

**411th FLASH REPORT ON
CENTRAL SECTOR PROJECTS
(Rs.150 crore and above)
January, 2020**



KUDANKULAM NUCLEAR POWER PROJECT UNIT-3



सत्यमेव जयते

Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division

Khurshid Lal Bhawan, Janpath
New Delhi-110001
Website: www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India Ltd.
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead Travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised Catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Operation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petroleum Corporation Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative Ltd.
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation Ltd.
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Corporation.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Corporation.
NCL	Northern Coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation Ltd.
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corporation Ltd.
NGN	Next Generation Network
NLC	Neyveli Lignite Corporation Ltd.
NMDC	National Mineral Development Corporation Ltd.
NPC	Nuclear Power Corporation Ltd.
NRL	Numaligarh Refinery Ltd.
OB	Over Burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over Bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India Ltd.
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

EXECUTIVE SUMMARY

1. The Flash Report for January 2020 contains information on the status of the 1692 Central Sector Infrastructure Projects costing ₹150 crore and above. During January 2020, 12 projects (1 project each from Fertilisers & Water Resources, 5 projects each from Petroleum and Power sector) have reported completion with completion Cost of Rs.10549.05 crore.

2. During the reference month, out of 1692 projects, 552 projects are delayed with respect to their original schedules and 101 projects have reported additional delays vis-à-vis their date of completion reported in the previous month. Of these 101 projects, 31 are Mega Projects costing ₹1000 crore and above.

S.No.	Sector	Projects on monitor (No.)	Delayed Projects w.r.t original schedule (No.)	Additionally delayed during the month under report (No.)	Additionally delayed Mega Projects (No.)
1	ROAD TRANSPORT AND HIGHWAYS	867	186	47	5
2	RAILWAYS	312	148	8	3
3	PETROLEUM	148	60	13	6
4	COAL	107	39	2	0
5	URBAN DEVELOPMENT	74	29	6	1
6	POWER	64	48	13	9
7	WATER RESOURCES	50	5	1	1
8	HEALTH AND FAMILY WELFARE	23	11	1	1
9	CIVIL AVIATION	13	4	0	0
10	STEEL	9	8	5	3
11	MINES	5	2	0	0
12	ATOMIC ENERGY	4	4	2	2
13	FERTILISERS	4	2	2	0
14	TELECOMMUNICATIONS	4	2	1	0
15	HUMAN RESOURCE DEVELOPMENT	4	1	0	0
16	COMMERCE AND INDUSTRY	2	2	0	0
17	HEAVY INDUSTRY	1	1	0	0
18	SHIPPING AND PORTS	1	0	0	0
Total		1692	552	101	31

3. Total original cost of implementation of the 1692 projects was ₹20,75,212.70 crore and their anticipated completion cost is likely to be ₹24,78,016.45 crore, which reflects overall cost overruns of ₹4,02,803.75 crore (19.41% of original cost). The expenditure incurred on these projects till January 2020 is ₹10,97,604.64 crore, which is 44.29% of the anticipated cost of the projects. The sector-wise list of projects (maximum five in numbers) having maximum percentage of cost overruns is as follows:-

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Percentage of Cost
Overruns (as on 01-02-2020)**

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (%)
ATOMIC ENERGY					
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	16580.00	44.69
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12320.00	17079.00	38.63
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6840.00	95.88
CIVIL AVIATION					
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	314.61	441.33	40.28
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	859.86	860.00	0.02
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	09/2015	338.93	339.00	0.02
COAL					
1	RANIGANJ MASTER PLAN	08/2009	2661.73	5146.48	93.35
2	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	06/2011	5907.11	7080.41	19.86
3	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.49	201.44
4	BHANEAGAON OC	02/2015	187.94	409.68	117.98
5	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	249.03	448.86	80.24
COMMERCE AND INDUSTRY					
1	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	4773.00	5178.00	8.49
HEALTH AND FAMILY WELFARE					
1	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR	03/2019	1577.00	1828.00	15.92
2	AIIMS BILASPUR	04/2018	1351.00	1471.00	8.88
3	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	499.23	20.55
4	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	585.00	15.71
5	AIIMS - MOTHER AND CHILD BLOCK	12/2013	204.44	270.00	32.07
HUMAN RESOURCE DEVELOPMENT					
1	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	09/2013	484.32	626.26	29.31
PETROLEUM					
1	VISAKH REFINERY MODERNISATION PROJECT	07/2016	20928.00	26264.00	25.50
2	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	2915.00	4915.00	68.61
3	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	05/2016	4497.00	6025.00	33.98
4	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	01/2015	1823.00	3027.90	66.09
5	PARADIP HYDERABAD PIPELINE	01/2015	2321.00	3338.00	43.82
POWER					
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19496.34	210.19
2	BARH STPP(3X660MW) NTPC	02/2005	8692.97	21312.11	145.16
3	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	9997.11	155.05
4	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	7927.34	217.49
5	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	01/2013	12964.60	17304.00	33.47
RAILWAYS					
1	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	16592.00	51101.00	207.99
2	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	27949.00	1017.96

3	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	11589.00	28181.00	143.17
4	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	4454.17	12524.00	181.17
5	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	8248.50	3230.57
ROAD TRANSPORT AND HIGHWAYS					
1	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2967.50	167.82
2	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	03/2016	1587.49	2982.00	87.84
3	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	08/2016	1388.34	2587.50	86.37
4	DELHI AGRA APPROVED LENGTH 180.0 KM	10/2012	1928.22	2945.00	52.73
5	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)	03/2018	1532.62	2499.00	63.05
SHIPPING AND PORTS					
1	JAL MARG VIKAS PROJECT	01/2018	4200.00	5369.18	27.84
STEEL					
1	NMDC INTEGRATED STEEL PLANT	01/2010	15525.00	23140.00	49.05
TELECOMMUNICATIONS					
1	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	84.97
2	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	01/2018	231.80	240.10	3.58
URBAN DEVELOPMENT					
1	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	19058.00	30.53
2	KOCHI METRO RAIL PROJECT	07/2012	5181.79	6218.14	20.00
3	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	2000.00	64.04
4	REDEVELOPMENT OF EAST KIDWAI NAGAR	06/2012	4264.00	4720.73	10.71
5	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1113.34	44.80
WATER RESOURCES					
1	POLAVARAM IRRIGATION PROJECT	02/2009	10151.04	55548.87	447.22

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overrun.

4. The sector wise list of projects (maximum five in numbers) having maximum cost overruns (COR) in absolute term is as below:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Cost Overruns (COR)
(as on 01-02-2020)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (Rs.Crore)
ATOMIC ENERGY					
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	16580.00	5121.00
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12320.00	17079.00	4759.00
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6840.00	3348.00
CIVIL AVIATION					
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	314.61	441.33	126.72
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	859.86	860.00	0.14

3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	09/2015	338.93	339.00	0.07
	COAL				
1	RANIGANJ MASTER PLAN	08/2009	2661.73	5146.48	2484.75
2	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	06/2011	5907.11	7080.41	1173.30
3	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.49	307.06
4	BHANEGAON OC	02/2015	187.94	409.68	221.74
5	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	249.03	448.86	199.83
	COMMERCE AND INDUSTRY				
1	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	4773.00	5178.00	405.00
	HEALTH AND FAMILY WELFARE				
1	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR	03/2019	1577.00	1828.00	251.00
2	AIIMS BILASPUR	04/2018	1351.00	1471.00	120.00
3	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	499.23	85.12
4	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	585.00	79.42
5	AIIMS - MOTHER AND CHILD BLOCK	12/2013	204.44	270.00	65.56
	HUMAN RESOURCE DEVELOPMENT				
1	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	09/2013	484.32	626.26	141.94
	PETROLEUM				
1	VISAKH REFINERY MODERNISATION PROJECT	07/2016	20928.00	26264.00	5336.00
2	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	2915.00	4915.00	2000.00
3	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	05/2016	4497.00	6025.00	1528.00
4	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	01/2015	1823.00	3027.90	1204.90
5	PARADIP HYDERABAD PIPELINE	01/2015	2321.00	3338.00	1017.00
	POWER				
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19496.34	13211.01
2	BARH STPP(3X660MW) NTPC	02/2005	8692.97	21312.11	12619.14
3	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	9997.11	6077.52
4	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	7927.34	5430.44
5	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	01/2013	12964.60	17304.00	4339.40
	RAILWAYS				
1	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	16592.00	51101.00	34509.00
2	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	27949.00	25449.00
3	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	11589.00	28181.00	16592.00
4	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	4454.17	12524.00	8069.83
5	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	8248.50	8000.84
	ROAD TRANSPORT AND HIGHWAYS				
1	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2967.50	1859.50
2	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	03/2016	1587.49	2982.00	1394.51
3	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	08/2016	1388.34	2587.50	1199.16
4	DELHI AGRA APPROVED LENGTH 180.0 KM	10/2012	1928.22	2945.00	1016.78
5	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)	03/2018	1532.62	2499.00	966.38
	SHIPPING AND PORTS				
1	JAL MARG VIKAS PROJECT	01/2018	4200.00	5369.18	1169.18

	STEEL				
1	NMDC INTEGRATED STEEL PLANT	01/2010	15525.00	23140.00	7615.00
	TELECOMMUNICATIONS				
1	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	11330.00
2	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	01/2018	231.80	240.10	8.30
	URBAN DEVELOPMENT				
1	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	19058.00	4458.00
2	KOCHI METRO RAIL PROJECT	07/2012	5181.79	6218.14	1036.35
3	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	2000.00	780.79
4	REDEVELOPMENT OF EAST KIDWAI NAGAR	06/2012	4264.00	4720.73	456.73
5	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1113.34	344.46
	WATER RESOURCES				
1	POLAVARAM IRRIGATION PROJECT	02/2009	10151.04	55548.87	45397.83

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overruns.

5. Out of the 1692 projects, 302 are on schedule, 552 are delayed, 401 projects reported cost overrun and 201 projects reported both time and cost overrun with respect to their original project implementation schedules. However, the number of delayed projects decreases to 451 if delay is calculated on the basis of latest schedule of completion. Further, for 824 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 552 delayed projects, 168 (30.43%) projects have overall delay in the range of 1 to 12 months, 125 (22.64%) projects have delay in the range of 13 to 24 months, 145 (26.27%) projects have delay in the range of 25 to 60 months and 114 (20.65%) projects have delay of 61 months and above. **The average time overrun in these 552 delayed projects is 39.71 months.** The sector wise list of projects (maximum five in numbers) having maximum time overruns (TOR) are as below:

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Time Overruns (TOR)
(as on 01-02-2020)**

SN	PROJECT	DOA	DOC ORIGINAL	DOC ANTICIPATED	TOR (IN MONTHS)
	ATOMIC ENERGY				
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	09/2010	10/2021	133
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016	03/2023	75
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	09/2021	69
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	03/2013	11/2020	11/2023	36
	CIVIL AVIATION				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	09/2018	06/2020	21
2	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	01/2016	03/2020	12/2020	9

3	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	11/2016	04/2020	12/2020	8
4	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	06/2018	02/2022	08/2022	6
COAL					
1	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	03/2010	03/2022	144
2	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	03/2012	03/2024	144
3	RAMAGUNDAM OC-II EXTENSION	12/2009	03/2012	03/2023	132
4	KULDA OCP (MAHANADI COALFIELDS LTD)	01/2005	03/2010	03/2020	120
5	CHURI BENTI UG (0.81 MTY)	08/2007	03/2011	03/2021	120
COMMERCE AND INDUSTRY					
1	DELHI MUMBAI INDUSTRIAL CORRIDOR	09/2011	09/2019	09/2020	12
2	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	12/2019	09/2020	9
FERTILISERS					
1	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA	01/2018	11/2019	05/2020	6
2	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL	01/2018	11/2019	05/2020	6
HEALTH AND FAMILY WELFARE					
1	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	11/2013	09/2020	82
2	AIIMS - MOTHER AND CHILD BLOCK	12/2013	05/2017	06/2020	37
3	AIIMS - OPD(NEW)	08/2014	05/2017	01/2020	32
4	NEIGRIHMS SHILLONG MEGHALYA	10/2016	05/2018	07/2020	26
5	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	07/2016	02/2018	03/2020	25
HEAVY INDUSTRY					
1	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	08/2016	09/2019	03/2020	6
HUMAN RESOURCE DEVELOPMENT					
1	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	09/2013	09/2014	12/2020	75
MINES					
1	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/2014	04/2021	12/2022	20
2	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU	09/2017	06/2019	12/2020	18
PETROLEUM					
1	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	12/2012	02/2022	110
2	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	05/2013	02/2020	81
3	INTEGRATED DEVELOPMENT OF B-127 FIELDS	12/2011	03/2015	03/2020	60
4	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	02/2017	10/2021	56
5	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	07/2011	03/2017	06/2020	39
POWER					
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	09/2010	08/2023	155
2	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	09/2009	12/2021	147
3	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009	06/2020	126
4	BARH STPP(3X660MW) NTPC	02/2005	10/2011	08/2021	118
5	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	08/2008	06/2013	12/2022	114

	RAILWAYS				
1	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	04/1998	03/2003	03/2030	324
2	BANGLORE - SATYAMANGALAM (NL)(SWR)	04/1996	03/2002	03/2024	264
3	MUNEERABAD-MAHABOONAGAR(NL),SCR	04/1997	03/2000	03/2021	252
4	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI- ULUBERIA(BIRSHIVPUR) AND PUJALI- BAHRAHAT NL	04/2010	03/2005	03/2025	240
5	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	11/2002	06/2022	235
	ROAD TRANSPORT AND HIGHWAYS				
1	SONAPUR TO GUWAHTI (AS-3)	12/2003	03/2008	08/2020	149
2	NALBARI T BIJNI (AS-7)	12/2003	04/2008	03/2020	143
3	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	08/2010	10/2010	06/2021	128
4	GWALIOR-JHANSI, NH-75	12/2003	12/2009	03/2020	123
5	DELHI/ HARYANA BORDER TO ROHTAK	04/2007	05/2010	03/2020	118
	STEEL				
1	NMDC INTEGRATED STEEL PLANT	01/2010	05/2015	07/2020	62
2	NEW SINTER PLANT AT BOKARO STEEL PLANT	03/2015	10/2017	06/2020	32
3	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	05/2015	12/2017	03/2020	27
4	COKE OVEN BATTERY-5	12/2011	12/2017	03/2020	27
5	INSTALLATION OF NEW HOT STRIP MILL AT RSP	04/2015	04/2018	01/2020	21
	TELECOMMUNICATIONS				
1	NETWORK FOR SPECTRUM	03/2012	07/2015	05/2020	58
2	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	01/2018	10/2018	02/2020	16
	URBAN DEVELOPMENT				
1	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	10/2012	03/2020	89
2	IRRIGATION WORK OF BAGMATI	10/2005	03/2015	03/2021	72
3	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	02/2014	03/2015	10/2020	67
4	MUMBAI METRO LINE 3 (COLABA-BANDRA- SEEPZ)	07/2013	01/2015	05/2020	64
5	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	09/2012	03/2016	09/2020	54
	WATER RESOURCES				
1	POLAVARAM IRRIGATION PROJECT	02/2009	03/2020	12/2021	21
2	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI	03/2017	08/2019	02/2020	6
3	SEWAGE TREATMENT PLANT FOR ASSI- BHU SEWERAGE DISTRICT AT RAMANA	02/2017	11/2019	02/2020	3
4	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA	02/2011	12/2019	03/2020	3
5	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR	02/2014	12/2019	02/2020	2

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further time overruns.

6. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in obtaining forest/environment clearances, lack of infrastructure support & linkages, delay in tie-up of project financing, delay in finalization of detailed engineering, change in scope, delay in tendering, ordering & equipment supply, law & order problems, geological surprises, pre-commissioning teething troubles and contractual issues.

7. The Online Computerized Monitoring System (OCMS) of this Ministry envisages monitoring of milestones of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The sector wise list of earliest projects (maximum five in numbers) without milestones are as below:-

**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Milestones
(as on 01-02-2020)**

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST ANTICIPATED (Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)	ORIGINAL DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
CIVIL AVIATION							
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	314.61	441.33	85.79	09/2018	06/2020
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	09/2015	338.93	339.00	213.50	06/2019	N.A.
3	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	01/2016	219.91	219.91	65.45	03/2020	12/2020
4	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	11/2016	233.38	233.38	84.73	04/2020	12/2020
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	859.86	860.00	232.44	03/2021	03/2021
COAL							
1	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	03/2015	513.63	513.63	175.30	12/2019	N.A.
2	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	03/2015	522.45	522.45	9.88	09/2019	N.A.
3	COAL PROJECT NAME JAMUNIA UG (0.84 MTY)	07/2016	409.87	409.87	19.96	03/2022	03/2022
4	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	07/2016	17237.00	17237.80	8596.47	11/2021	11/2021
5	KOLAR PIMPRI EXTENSION OC	03/2017	362.73	362.73	322.62	03/2020	03/2020
COMMERCE AND INDUSTRY							
1	DELHI MUMBAI INDUSTRIAL CORRIDOR	09/2011	12579.09	12579.09	778.93	09/2019	09/2020
2	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	4773.00	5178.00	1309.65	12/2019	09/2020
HEALTH AND FAMILY WELFARE							
1	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	499.23	337.32	11/2013	09/2020

2	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	07/2016	703.00	557.48	327.76	06/2020	10/2020
3	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	07/2016	785.00	715.06	385.77	04/2020	10/2020
4	CNCI KOLKATA WEST BENGAL	08/2016	244.00	248.00	224.92	09/2018	05/2019
5	NEIGRIHMS SHILLONG MEGHALYA	10/2016	363.99	363.99	219.50	05/2018	07/2020
	HEAVY INDUSTRY						
1	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	08/2016	1554.00	1554.00	716.25	09/2019	03/2020
	HUMAN RESOURCE DEVELOPMENT						
1	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	09/2013	484.32	626.26	0.00	09/2014	12/2020
2	STUDY IN INDIA	03/2018	150.00	150.00	0.00	04/2018	N.A.
3	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION	08/2018	418.00	418.00	110.00	03/2019	N.A.
4	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA.	05/2019	303.90	303.90	0.00	03/2020	03/2020
	PETROLEUM						
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	1549.85	01/2012	N.A.
2	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	07/2011	350.00	350.00	2.06	01/2019	N.A.
3	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	678.00	678.00	8.10	02/2017	10/2021
4	ENNORE-TRICHY-MADURAI LPG PIPELINE	05/2013	711.00	711.00	11.12	06/2020	06/2020
5	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM	07/2014	247.00	247.00	0.00	03/2021	03/2021
	POWER						
1	LOKTAK D/S HEP(NHPC)	12/1999	578.62	578.62	0.00	06/2006	N.A.
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19496.34	11842.12	09/2010	08/2023
3	PAKRI BARWADIH COAL MINING PROJECT	10/2004	4237.96	4552.00	3365.00	10/2017	N.A.
4	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	01/2014	374.63	374.63	224.83	04/2016	03/2020
5	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	4754.42	9072.36	1402.48	12/2018	12/2020
	RAILWAYS						

1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	393.46	1026.00	182.49	03/2007	N.A.
2	NANGALDAM-TALWARA(NL),NR	03/1981	450.00	2200.00	668.77	07/2012	03/2024
3	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	297.32	614.00	275.07	03/2019	03/2020
4	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	04/1987	406.99	545.70	148.49	03/2006	03/2025
5	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	332.15	546.71	541.43	07/2014	N.A.
ROAD TRANSPORT AND HIGHWAYS							
1	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	01/1991	478.35	478.35	0.00	N.A.	N.A.
2	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	01/1991	319.68	369.77	113.67	N.A.	N.A.
3	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	01/1991	219.40	219.40	0.00	01/2018	N.A.
4	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	282.41	322.01	278.45	08/2016	N.A.
5	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	358.22	377.64	325.19	10/2016	N.A.
SHIPPING AND PORTS							
1	JAL MARG VIKAS PROJECT	01/2018	4200.00	5369.18	1540.69	03/2023	03/2023
TELECOMMUNICATIONS							
1	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	12146.00	07/2015	05/2020
2	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	06/2016	418.26	418.26	367.04	06/2017	N.A.
3	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	01/2018	231.80	240.10	119.92	10/2018	02/2020
URBAN DEVELOPMENT							
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1113.34	1085.64	02/2014	N.A.
2	IRRIGATION WORK OF BAGMATI	10/2005	956.00	956.00	651.21	03/2015	03/2021
3	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	175.94	176.65	12/2015	N.A.

4	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	08/2007	246.90	246.90	0.00	N.A.	N.A.
5	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	202.61	227.00	199.95	12/2016	N.A.
WATER RESOURCES							
1	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA	02/2011	279.91	279.91	199.59	12/2019	03/2020
2	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR	02/2014	274.76	274.76	171.80	12/2019	02/2020
3	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	225.77	225.77	183.57	03/2020	03/2020
4	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE	12/2014	272.32	272.32	191.36	04/2020	04/2020
5	SAIDPUR SEWER NETWORK PATNA	04/2015	268.63	268.63	192.80	01/2021	01/2021

N.A.: Not Available.

N.B.: The concerned administrative Ministry may like review these Projects in order to firm-up milestones.

9. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The sector wise list of earliest (oldest) projects (maximum five in numbers) without revised cost estimates are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Cost Estimates (as on 01-02-2020)

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST REVISED(Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	5677.00	5862.38
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	0.00	14629.00
COAL					
1	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	249.03	0.00	326.69
2	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	172.08	0.00	377.07
3	BHUBANESWARI OCP, MCL (20.0 MTY)	12/2007	490.10	0.00	524.33
4	KANIHA OCP, MCL, (10.0 MTY)	12/2007	457.77	0.00	568.14
5	ANANTA OC EXPANSION PH-III (15.0 MTY)	08/2008	207.28	0.00	306.94
HEALTH AND FAMILY WELFARE					
1	AIIMS - MOTHER AND CHILD BLOCK	12/2013	204.44	0.00	210.75
2	AIIMS - OPD(NEW)	08/2014	293.65	0.00	304.62
3	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	0.00	586.96
4	CONSTRUCTION OF HOSPITAL BLOCK, IIT,	12/2014	168.90	0.00	169.51

	KHARAGPUR				
	PETROLEUM				
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	0.00	1549.85
2	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	0.00	1386.15
3	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL	05/2016	664.00	0.00	664.73
	POWER				
1	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	0.00	7761.19
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	0.00	11842.12
3	BRBCL-NABINAGAR TPP- JV (4X250 MW)	01/2007	5353.00	7998.00	8056.25
4	MUNPL-MEJA TPP - JV (2X660 MW)	04/2012	9750.89	0.00	10103.00
5	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	12/2012	11846.00	0.00	12826.56
	RAILWAYS				
1	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	04/1991	329.39	803.11	1060.33
2	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	09/1995	303.98	0.00	683.11
3	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	02/1996	268.87	0.00	927.86
4	NANDYAL-YERRAGUNTALA(NL),SCR	03/1996	164.36	0.00	999.64
5	HARIDASPUR-PARADEEP(NL)	04/1996	1185.64	0.00	1883.44
	ROAD TRANSPORT AND HIGHWAYS				
1	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	217.61	0.00	454.21
2	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	160.00	0.00	223.81
3	NALBARI T BIJNI (AS-7)	12/2003	208.00	0.00	340.21
4	NALBARI TO BIJNI (AS-6)	12/2003	225.00	0.00	328.47
5	TRICHY - KARUR	03/2007	516.00	0.00	886.96
	STEEL				
1	INSTALLATION OF NEW HOT STRIP MILL AT RSP	04/2015	3127.30	0.00	3201.42
	URBAN DEVELOPMENT				
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1070.97	1085.64
2	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	173.00	176.65
3	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	0.00	16352.87
4	KOCHI METRO RAIL PROJECT	07/2012	5181.79	5687.79	5817.11
5	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	02/2014	156.57	0.00	159.35

N.B.: The concerned administrative Ministry may like to review these Projects in order to firm-up revised cost estimates.

10. The sector wise list of earliest projects (maximum five in numbers) without revised commissioning schedule are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Commissioning Schedule (as on 01-02-2020)

SN	SECTOR/ PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	REVISED DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
CIVIL AVIATION					
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	09/2015	06/2019	N.A.	N.A.
COAL					
1	KAKATIYA LONGWALL	12/2008	12/2012	N.A.	N.A.
2	MANUGURU OC-II EXTENSION PHASE-II	03/2010	03/2012	N.A.	N.A.
3	MURAIIDH UG TURN-KEY PROJECT	02/2011	04/2014	N.A.	N.A.
4	KAPURIA UG(PSLW)	08/2011	04/2017	N.A.	N.A.
5	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	04/2013	06/2015	N.A.	N.A.
FERTILISERS					
1	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT	01/2018	11/2019	N.A.	11/2019
HEALTH AND FAMILY WELFARE					
1	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	03/2018	N.A.	09/2019
2	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	05/2017	N.A.	07/2019
3	CNCI KOLKATA WEST BENGAL	08/2016	09/2018	N.A.	05/2019
HUMAN RESOURCE DEVELOPMENT					
1	STUDY IN INDIA	03/2018	04/2018	N.A.	N.A.
2	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION	08/2018	03/2019	N.A.	N.A.
PETROLEUM					
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	01/2012	N.A.	N.A.
2	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	07/2011	01/2019	N.A.	N.A.
3	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	09/2012	03/2015	N.A.	N.A.
4	RESID UPGRADATION PROJECT	03/2013	11/2015	N.A.	N.A.
5	120 TMTA LPG BOTTLING PLANT AT GORAKHPUR UP	03/2014	09/2019	N.A.	N.A.
POWER					
1	LOKTAK D/S HEP(NHPC)	12/1999	06/2006	N.A.	N.A.
2	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017	N.A.	N.A.
3	MOUDA STPP STAGE 2	03/2012	09/2016	N.A.	N.A.
4	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	07/2012	08/2017	N.A.	N.A.
5	TALAIPALLI COAL MINING PROJECT	09/2015	11/2019	N.A.	11/2019
RAILWAYS					
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	03/2007	03/2007	N.A.
2	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	07/2014	N.A.	N.A.
3	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	02/1996	03/2005	N.A.	N.A.
4	NANDYAL-YERRAGUNTLA(NL),SCR	03/1996	02/2009	N.A.	N.A.
5	ETAWAH-MAINPURI (NL),NCR	04/1997	12/2008	N.A.	N.A.
ROAD TRANSPORT AND HIGHWAYS					

1	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O	01/1991	04/2014	N.A.	N.A.
2	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	08/2016	N.A.	N.A.
3	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	10/2016	N.A.	N.A.
4	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB	01/1991	10/2017	N.A.	N.A.
5	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	01/1991	01/2018	N.A.	N.A.
TELECOMMUNICATIONS					
1	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY	09/2014	09/2014	N.A.	N.A.
2	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	06/2016	06/2017	N.A.	N.A.
URBAN DEVELOPMENT					
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	02/2014	N.A.	N.A.
2	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	12/2015	N.A.	N.A.
3	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	08/2007	N.A.	N.A.	N.A.
4	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND	12/2007	06/2016	N.A.	N.A.
5	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016	N.A.	N.A.
WATER RESOURCES					
1	INTERCEPTION AND DIVERSION (I&D)WITH STP AT RISHIKESH	03/2017	11/2019	N.A.	N.A.
2	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA	03/2017	12/2019	N.A.	N.A.

N.A.: Not Available.

N.B.: The concerned administrative Ministry may like to review these Projects in order to firm-up revised commissioning schedule.

11. The status as on 01.02.2020 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

12. This has the approval of Competent Authority, Ministry of Statistics and Programme Implementation.

TABLE-1

EXECUTIVE SUMMARY COSTING Rs. 150 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	867	47
2	RAILWAYS	312	8
3	PETROLEUM	148	13
4	COAL	107	2
5	URBAN DEVELOPMENT	74	6
6	POWER	64	13
7	WATER RESOURCES	50	1
8	HEALTH AND FAMILY WELFARE	23	1
9	CIVIL AVIATION	13	0
10	STEEL	9	5
11	MINES	5	0
12	ATOMIC ENERGY	4	2
13	FERTILISERS	4	2
14	TELECOMMUNICATIONS	4	1
15	HUMAN RESOURCE DEVELOPMENT	4	0
16	COMMERCE AND INDUSTRY	2	0
17	HEAVY INDUSTRY	1	0
18	SHIPPING AND PORTS	1	0
	Total	1692	101

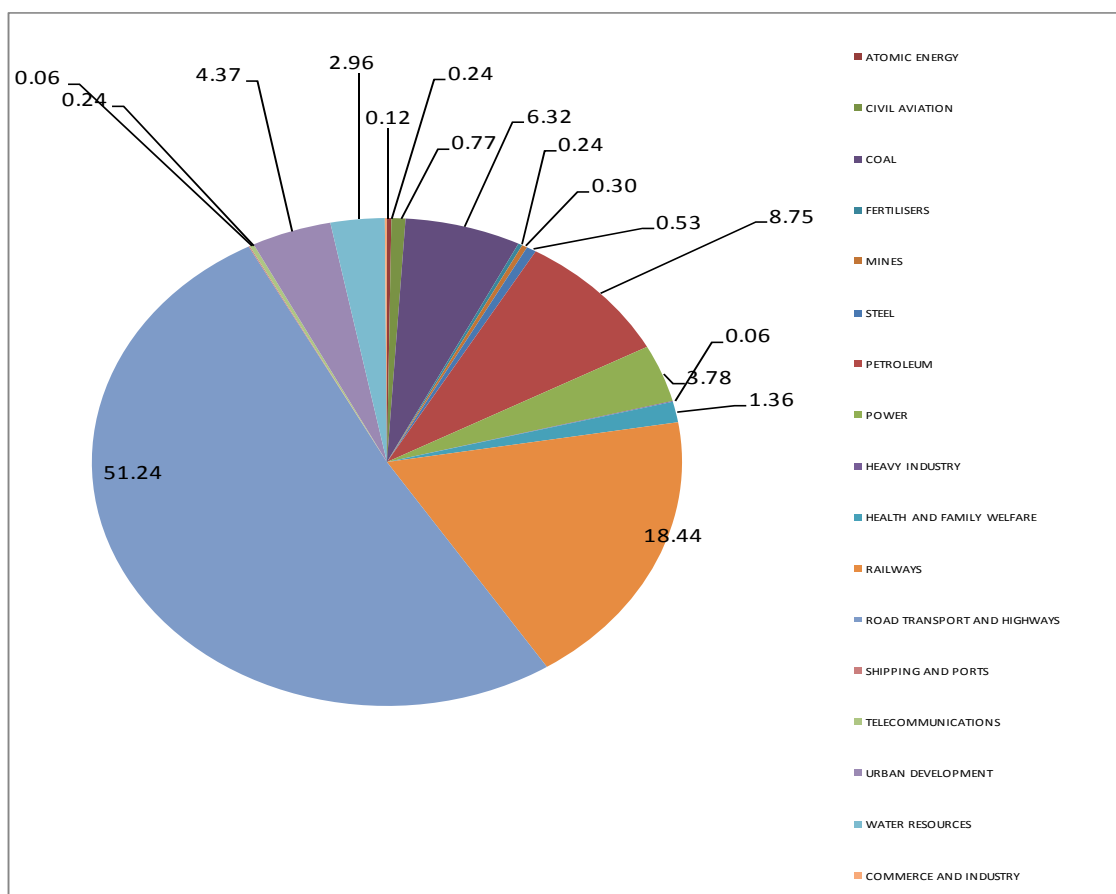


TABLE-2

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2019-2020				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2019			
	<u>COAL</u>			
1	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI (NORTHERN COAL FIELDS LIMITED) - [N06000033]	259.40	03/2012	266.38
2	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) (NORTHERN COAL FIELDS LIMITED) - [N06000091]	1,131.28	03/2018	796.85
	<u>PETROLEUM</u>			
3	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000175]	3,076.00	09/2017	3,450.30
	<u>POWER</u>			
4	BONGAIGAON THERMAL POWER PROJECT (NATIONAL THERMAL POWER CORPORATION) - [N18000041]	4,375.35	10/2011	7,000.00
5	TRIPURA GAS BASED POWER PROJECT (NORTH EAST ELECTRIC POWER CORPORATION) - [N18000071]	421.01	07/2013	963.23
	<u>RAILWAYS</u>			
6	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) RAILWAY) - [N22000113]	653.19	03/2014	862.17
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
7	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000357]	567.51	03/2018	421.60
	May,2019			
	<u>COAL</u>			
8	MAKARDHOKRA I OC (WESTERN COAL FIELDS LIMITED) - [N06000119]	266.23	03/2021	144.38
	<u>PETROLEUM</u>			
9	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000084]	736.65	09/2011	331.47
10	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY Central Sector Projects(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000290]	474.15	05/2019	348.64
	<u>POWER</u>			

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2019-2020

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
11	WESTERN REGION STRENGTHENING SCHEME-V (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000035]	477.69	09/2010	691.96
12	KUDGI STPP STAGE 1 (NATIONAL THERMAL POWER CORPORATION) - [N18000131]	15,166.19	01/2017	15,364.00
13	SOLAPUR STPP (NATIONAL THERMAL POWER CORPORATION) - [N18000133]	9,395.18	01/2017	8,617.00
14	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000158]	539.82	06/2016	434.33
15	FGUTPP, UNCHAHAH STAGE-IV (1X500 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000174]	3,363.12	12/2016	2,244.00
16	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000222]	790.13	06/2019	575.24
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
17	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000145]	1,585.00	05/2013	2,023.33
18	JORBAT - BARAPANI PPP (ANNUITY)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000180]	536.00	01/2014	845.41
19	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S EPC) - [N24000241]	177.18	03/2016	40.51
20	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTION EPC) - [N24000242]	158.65	03/2016	103.50
21	YAN TO NIRMAL SEREHALITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW EPC) - [N24000243]	244.08	03/2016	38.32
22	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T EPC) - [N24000244]	340.00	03/2016	2.00
23	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO EPC) - [N24000246]	244.30	12/2016	2.00
24	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S) - [N24000249]	218.31	12/2015	208.28
25	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337) - [N24000250]	260.39	11/2016	188.00
26	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 EPC) - [N24000255]	220.72	11/2016	155.30
27	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 EPC) - [N24000261]	267.16	11/2017	308.33
28	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUEDEM TO A EPC) - [N24000262]	201.12	02/2015	150.19
29	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]	241.61	02/2017	178.94
30	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN EPC) - [N24000265]	297.78	02/2017	284.89
31	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC) - [N24000266]	361.30	07/2014	203.29
32	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) EPC) - [N24000267]	258.99	07/2014	200.44

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2019-2020

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
33	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC EPC() - [N24000268]	251.55	02/2015	172.65
34	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T EPC() - [N24000269]	175.03	-	152.53
35	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP EPC() - [N24000272]	266.00	-	182.13
36	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000273]	314.43	-	216.96
37	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA ITEM RATE(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000277]	185.82	-	142.23
38	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. EPC() - [N24000278]	213.47	03/2015	182.91
39	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV EPC() - [N24000279]	298.34	03/2015	269.93
40	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I EPC() - [N24000280]	262.54	03/2015	215.11
41	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- ITEM RATE() - [N24000283]	169.26	12/2012	280.72
42	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO EPC() - [N24000284]	170.21	11/2014	140.09
43	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. EPC() - [N24000286]	394.20	-	332.62
44	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000288]	422.34	-	406.40
45	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE EPC() - [N24000289]	435.90	-	380.41
46	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 EPC() - [N24000290]	279.68	-	286.96
47	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO EPC() - [N24000291]	463.65	-	536.84
48	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM EPC() - [N24000292]	573.96	-	557.08
49	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000293]	480.21	-	372.37
50	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 EPC() - [N24000299]	224.83	05/2015	189.85
51	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU EPC() - [N24000300]	309.01	09/2015	391.89
52	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION EPC() - [N24000303]	417.61	06/2014	261.29

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2019-2020

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
53	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 EPC() - [N24000310]	377.83	07/2017	318.66
54	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO EPC(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000329]	497.89	04/2017	735.92
55	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000330]	629.74	-	721.04
56	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000336]	227.74	10/2016	187.85
57	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000369]	269.26	10/2016	212.72
58	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI EPC() - [N24000370]	483.38	-	470.16
59	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 EPC() - [N24000372]	616.36	-	554.68
60	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(EPC() - [N24000374]	486.74	-	415.58
61	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000377]	397.04	10/2016	368.49
62	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP BOT (TOLL)() - [N24000381]	257.80	02/2016	59.30
63	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(EPC() - [N24000383]	312.79	-	258.86
64	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOULA BYPASS(EXISTING KM.138.030 TO K EPC() - [N24000384]	319.80	-	289.40
65	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' ITEM RATE() - [N24000387]	264.16	-	533.18
66	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA ITEM RATE() - [N24000390]	1,494.48	02/2011	2,158.50
67	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000393]	774.57	03/2018	613.58
68	SHAHDOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 EPC() - [N24000394]	532.49	05/2017	386.02
69	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000399]	317.76	03/2017	344.30
70	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000403]	283.45	10/2016	285.18
71	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM EPC() - [N24000404]	578.38	-	481.30

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2019-2020

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
72	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA EPC() - [N24000405]	789.83	-	608.55
73	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARALI ITEM RATE(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000406]	208.87	05/2016	206.78
74	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM ITEM RATE(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000409]	176.22	02/2018	0.10
75	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A EPC() - [N24000410]	641.02	12/2017	449.66
76	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 EPC() - [N24000416]	224.83	04/2015	189.85
77	SONOLI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000418]	493.94	03/2017	503.25
78	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA ITEM RATE() - [N24000419]	165.00	09/2010	174.57
79	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF ITEM RATE() - [N24000420]	104.00	09/2010	218.29
80	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 EPC(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000421]	235.08	05/2018	235.08
81	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP BOT (TOLL)() - [N24000447]	670.82	02/2015	590.00
82	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A () - [N24000474]	327.32	05/2017	301.41
83	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000476]	273.06	-	199.72
84	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000512]	207.88	-	179.58
85	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO EPC() - [N24000526]	899.21	-	748.74
86	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000529]	207.88	-	179.58
87	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000536]	377.64	03/2014	755.28
88	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO () - [N24000538]	292.98	11/2014	160.96
89	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR- HYDERABAD SECTION NS-60 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000561]	244.00	07/2018	231.90
90	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000573]	322.01	08/2014	267.00

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2019-2020

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
91	FUNDED)2 LANING FROM CHANGLANG DISTRICT BOUNDARY - KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000615]	334.22	06/2016	334.22
92	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000647]	162.51	05/2016	136.31
93	WIDENING TO 2 LANE WITH PAVED SHOULDER AND STRENGTHENING FROM KM 88 TO 130 ON NH-86 () - [N24000856]	170.00	02/2015	115.57
94	REHABILITATION AND UPGRADATION OF PURANPUR - KHUTAR SECTION FROM KM 38.00 TO KM 82.00 OF NH-730 TO 2 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001142]	225.96	06/2018	174.63
	June,2019			
	<u>RAILWAYS</u>			
95	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) (NORTH CENTRAL RAILWAY) - [220100007]	158.77	03/1994	682.34
96	AMRAVATI-NARKHER NL(CR) (CENTRAL RAILWAYS) - [220100118]	663.01	06/1999	726.33
97	CALICUT-MANGALORE (DL) (SR) (SOUTHERN RAILWAY) - [220100151]	240.00	-	0.01
98	MANDARHILL-DUMKA-RAMPURHAT (NL),ER (EASTERN RAILWAYS) - [220100168]	1,125.89	03/2016	1,180.08
99	KARUR-SALEM(NL),SR (SOUTHERN RAILWAY) - [220100191]	155.55	-	863.54
100	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR (NORTH CENTRAL RAILWAY) - [220100243]	108.00	12/2009	455.39
101	KATIHAR - JOGBANI (GC)(NEFR) (NORTH EAST FRONTIER RAILWAY) - [220100247]	792.46	12/2010	944.80
102	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) (NORTH EASTERN RAILWAY) - [220100256]	744.71	-	917.49
103	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) (SOUTHERN RAILWAY) - [220100263]	280.00	-	942.28
104	JIND-SONEPAT (NL),NR (NORTHERN RAILWAY) - [220100280]	238.56	03/2012	785.75
105	KODERMA GIRIDH (NL), ECR (EAST CENTRAL RAILWAYS) - [220100306]	768.87	-	988.38
106	MAHARAJGANJ-MASRAKH (NL) - NER (NORTH EASTERN RAILWAY) - [220100316]	218.19	06/2018	380.50
107	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) (RAIL VIKAS NIGAM LTD.) - [N22000049]	732.81	03/2008	2,191.46
108	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE (SOUTHERN RAILWAY) - [N22000080]	343.17	-	1,110.44
109	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) (NORTHERN RAILWAY) - [N22000088]	369.90	03/2010	891.24
110	AGARTALA SABROOM, NL, NEFR (NORTH EAST FRONTIER RAILWAY) - [N22000099]	1,142.00	03/2014	3,354.18
111	DAKSHIN-BARASAL-LAKSHMIKANTAPUR (EASTERN RAILWAYS) - [N22000116]	259.51	02/2012	148.37
112	GHUTIASARIF-CANNING (ER) (EASTERN RAILWAYS) - [N22000117]	193.08	12/2011	154.30

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2019-2020

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
113	PANDABESWAR-CHINPAI DOUBLING (ER) (EASTERN RAILWAYS) - [N22000118]	293.74	12/2010	128.78
114	BHOJIPUR TANAKPUR VIA PILIBHIT (NORTH EASTERN RAILWAY) - [N22000132]	195.64	-	450.62
115	AUNRIHAR MANDUADIH (NORTH EASTERN RAILWAY) - [N22000133]	199.75	08/2018	287.33
116	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING (SOUTH EASTERN RAILWAY) - [N22000164]	309.44	12/2015	529.27
117	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC (SOUTHERN RAILWAY) - [N22000188]	271.24	-	468.58
118	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA (NORTH EAST FRONTIER RAILWAY) - [N22000194]	895.00	03/2007	1,566.57
119	CHENGANNUR-CHINGAVANAM (SOUTHERN RAILWAY) - [N22000203]	191.72	-	447.03
120	LUMDING-HOJAI PATCH DOUBLING PROJECT (NORTH EAST FRONTIER RAILWAY) - [N22000211]	246.07	03/2019	490.29
121	MEERUT-MUZAFARNAGAR PATCH DL (NORTHERN RAILWAY) - [N22000267]	377.44	-	430.12
122	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH (NORTHERN RAILWAY) - [N22000290]	338.54	-	384.61
123	JAKHAL-MANSA DOUBLING ON SPR SECTION (NORTHERN RAILWAY) - [N22000291]	162.96	-	160.25
124	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI (SOUTHERN RAILWAY) - [N22000303]	460.94	01/1999	0.01
125	MADURAI - RAMESWARAM (161 KM) GAUGE CONVERSION (SOUTHERN RAILWAY) - [N22000439]	458.63	03/2015	367.71
126	TRICHY - MANAMADURAI (150 KM) GAUGE CONVERSION (SOUTHERN RAILWAY) - [N22000440]	200.84	03/2014	394.51
127	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION (SOUTHERN RAILWAY) - [N22000446]	600.00	03/2010	673.80
128	MADURAI-DINDIGUL (INCL. AMBADUTURAI-KODAIKANAL ROAD) (62.05 KM) DOUBLING (SOUTHERN RAILWAY) - [N22000450]	199.55	03/2009	238.61
129	MANAMADURAI - VIRUDHUNAGAR (66.55 KM) GAUGE CONVERSION. (SOUTHERN RAILWAY) - [N22000453]	208.00	03/2012	206.20
130	MULANTURUTTI - KURUPPANTARA (24 KM) DOUBLING. (SOUTHERN RAILWAY) - [N22000454]	241.00	03/2014	293.37
131	GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW (NORTH EASTERN RAILWAY) - [N22000455]	233.00	04/1999	349.37
132	MANDHANA - BRAHMAWART NEW LINE PROJECT. (NORTH EASTERN RAILWAY) - [N22000458]	609.04	04/1999	1,806.84
133	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM (EAST CENTRAL RAILWAYS) - [N22000474]	624.47	02/2016	3,376.08
	July, 2019			
	<u>COAL</u>			
134	NORTH URIMARI OCP (3.0 MTY) (CENTRAL COAL FIELDS LIMITED) - [N06000084]	179.87	03/2012	163.23

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2019-2020				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	<u>STEEL</u>			
135	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) (RASTRIYA ISPAT NIGAM LIMITED) - [N12000120]	465.85	07/2018	390.25
	<u>PETROLEUM</u>			
136	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I (GAS AUTHORITY OF INDIA LIMITED) - [N16000072]	3,957.00	12/2018	2,707.26
137	PARADIP-RAIPUR- RANCHI PIPELINE (INDIAN OIL CORPORATION LIMITED) - [N16000088]	1,793.00	12/2016	1,788.86
138	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) (INDIAN OIL CORPORATION LIMITED) - [N16000187]	191.96	05/2015	76.28
139	REPLACEMENT OF KV SECTION OF KSPL Central Sector Projects(INDIAN OIL CORPORATION LIMITED) - [N16000287]	279.00	08/2018	200.05
	<u>POWER</u>			
140	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) (SATLUJ JAL VIDYUT NIGAM LIMITED) - [N18000235]	330.00	11/2017	331.46
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
141	BHOPAL-BIORA (4L) OF NH-12 IN MP BOT (TOLL)() - [N24000380]	704.26	05/2015	5.21
	<u>TELECOMMUNICATIONS</u>			
142	MADHYA PRADESH ACCESS (LOT1) Central Sector Projects(BHARAT SANCHAR NIGAM LIMITED) - [N26000110]	215.30	05/2018	33.46
	August,2019			
	<u>COAL</u>			
143	AMLAI OC EXPANSION SECTOR B (1.50 MTY) (SOUTH-EASTERN COAL FIELDS LIMITED) - [N06000082]	198.59	03/2016	169.15
144	GOKUL (WESTERN COAL FIELDS LIMITED) - [N06000120]	267.67	03/2018	209.47
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
145	IMPROVEMENT FROM KM 0/0 TO 68/0 EPC() - [N24000413]	319.80	10/2016	268.01
146	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000642]	226.31	10/2017	137.43
147	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000643]	319.80	05/2016	268.27

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2019-2020				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
148	WIDENING TO 2L/2LPS FROM 131/0 TO 192/0 (BHOJPUR TO CHHATABAR) OF NH-200 UNDER NHIP IN ODISHA (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000918]	251.92	10/2015	225.98
149	WIDENING TO 2L/2LPS FROM 25/0 TO 80/0 (NABARANGPUR TO KOKSARA) OF NH-201 UNDER NHIP IN ODISHA (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000919]	265.35	10/2015	247.56
150	WIDENING TO 2L FROM 228/70 TO 258/70 AND 286/70 TO 327/70 OF VR ROUTE UNDER VRC IN ODISHA (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000924]	229.29	11/2015	163.40
151	REHABILITATION AND UPGRADATION OF EEPURUPALEM-ONGOLE SECTION FROM KM195.000 TO 254.500 OF NH214A(NH2 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000971]	574.19	07/2017	456.98
	September,2019			
	<u>PETROLEUM</u>			
152	URAN CHAKAN SHIKRAPUR LPG PIPELINE (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000155]	309.81	10/2014	712.26
153	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000237]	407.00	09/2019	391.85
	October,2019			
154	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000248]	822.66	11/2018	822.02
155	BRANCH PIPELINE OF PAJPL TO UNA (INDIAN OIL CORPORATION LIMITED) - [N16000250]	151.00	09/2019	147.35
156	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000280]	420.76	09/2018	239.45
	<u>POWER</u>			
157	EASTERN REGION STRENGTHENING SCHEME -IX (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000171]	196.58	02/2016	165.87
158	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000180]	268.80	03/2018	259.49
159	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000227]	1,429.38	01/2019	1,050.46
160	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000236]	251.60	06/2019	192.74
161	WESTERN REGION STRENGTHENING SCHEME XVIII (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000241]	195.05	02/2020	120.83
	November,2019			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2019-2020

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
162	2 LANNING OF MOKAMA-MUNGER PPP (ANNUITY)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000166]	351.54	05/2013	329.40
163	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000446]	788.51	03/2018	103.37
164	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000450]	785.78	03/2018	839.00
165	NAGPUR - KONDHALI (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000472]	168.00	06/2006	226.24
166	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000609]	771.18	-	261.77
	December,2019			
	<u>PETROLEUM</u>			
167	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE (INDIAN OIL CORPORATION LIMITED) - [N16000195]	890.00	10/2019	609.29
168	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000209]	310.00	03/2013	17.84
	<u>URBAN DEVELOPMENT</u>			
169	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000076]	157.84	03/2017	167.23
170	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000107]	188.00	06/2019	146.45
	January,2020			
	<u>FERTILISERS</u>			
171	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY (RASHTRIYA CHEMICAL & FERTILISER LIMITED) - [N08000009]	197.79	11/2016	188.89
	<u>PETROLEUM</u>			
172	ASSAM RENEWAL PROJECT FOR GROUP A (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000061]	2,465.15	03/2013	2,177.58
173	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000127]	202.94	01/2014	193.03
174	POLYPROPYLENE PLANT AT PARADIP REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000179]	3,150.00	09/2017	2,573.02
175	DEVELOPMENT OF BSE-11 BLOCK Central Sector Projects(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000293]	511.30	11/2019	546.76

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2019-2020				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
176	4TH PHASE DEVELOPMENT OF NBP FIELD Central Sector Projects(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000294]	968.61	11/2019	968.11
	<u>POWER</u>			
177	KUNADANKULAM APP TRANS SYSTEM (PGCIL) (POWER GRID CORPORATION OF INDIA LIMITED) - [180100258]	1,779.29	11/2008	2,294.33
178	DHUKWAN SMALL HYDRO PROJECT (THDC INDIA LIMITED) - [N18000189]	195.42	02/2014	322.23
179	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000223]	844.64	04/2019	437.95
180	SOUTHERN REGION STRENGTHENING SCHEME-XXI (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000233]	562.25	03/2019	423.45
181	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000248]	337.75	06/2019	176.71
	<u>WATER RESOURCES</u>			
182	SEWERAGE WORKS IN SEWERAGE DISTRICT A OF ALLAHABAD (Uttar Pradesh Jal Nigam) - [N300000005]	288.94	09/2019	246.99

TABLE-3

Month wise List of Deleted Projects Costing Rs. 150 crore and above during				
2019-2020				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	June,2020			
	<u>RAILWAYS</u>			
1	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL (RAIL VIKAS NIGAM LTD.) - [220100149]	631.78	12/2012	762.72
2	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR (NORTHERN RAILWAY) - [220100258]	625.30	06/2007	848.84
3	TAMLUK DIGHA,LINE DOUBLING (SER) (SOUTH EASTERN RAILWAY) - [N22000097]	293.97	06/2005	0.00
4	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) (NORTH WESTERN RAILWAY) - [N22000112]	829.74	03/2015	823.85
5	SANTOSH PUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE (EASTERN RAILWAYS) - [N22000248]	268.52	-	0.00
6	MUNIRABAD (GINGERA) -RAICHUR NL (SOUTH WESTERN RAILWAY) - [N22000257]	179.65	-	940.47
7	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL (NORTHERN RAILWAY) - [N22000268]	396.04	-	225.18
8	CHANDIGARH-BADDI NL (NORTHERN RAILWAY) - [N22000296]	328.14	-	233.84
9	MM FROM BURAMARA-CHAKULIA (SOUTH EASTERN RAILWAY) - [N22000305]	466.48	-	0.83
10	MIRAJ-LONDA (SOUTH WESTERN RAILWAY) - [N22000327]	1,830.00	-	254.57
11	CHHINDWARA-MANDLA FORT GC (SOUTH EAST CENTRAL RAILWAY) - [N22000481]	556.54	03/2012	0.00
12	KENDRI-DHAMTARI INCLUDING ABHANPUR-RAJIM (SOUTH EAST CENTRAL RAILWAY) - [N22000482]	1,471.93	03/2022	0.00
	<u>WATER RESOURCES</u>			
13	PAGLADIYA DAM PROJECT (MINISTRY OF WATER RESOURCES) - [300100001]	542.90	12/2007	0.00
	July,2020			
	<u>STEEL</u>			
14	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000085]	188.93	04/2015	138.83
15	REVAMPING OF SINTER MACHINES - 1 AND 2 (RASTRIYA ISPAT NIGAM LIMITED) - [N12000091]	343.00	10/2016	254.65
16	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000097]	4,749.00	09/2017	110.95

Month wise List of Deleted Projects Costing Rs. 150 crore and above during

2019-2020

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
17	2 MTPA PELLET PLANT AT NAGARNAR (NATIONAL MINERAL DEVELOPMENT CORPORATION (NMDC)) - [N12000115]	818.00	06/2020	31.60
	<u>RAILWAYS</u>			
18	BHADUTOLA-JHARGRAM VIA LALGARH (NL) (SOUTH EASTERN RAILWAY) - [N22000161]	289.64	-	0.13
19	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI (NORTHERN RAILWAY) - [N22000270]	654.00	-	0.00
20	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR (NORTHERN RAILWAY) - [N22000271]	1,239.00	-	0.00
21	HISSAR-SIRSA VIA AGROHA AND FATEHABAD (NORTHERN RAILWAY) - [N22000292]	400.00	-	0.00
22	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH (NORTHERN RAILWAY) - [N22000293]	876.00	-	0.00
23	MM FROM PANSKURA-GHATAL NL (SOUTH EASTERN RAILWAY) - [N22000309]	276.69	-	0.00
24	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI(SOUTH EASTERN RAILWAY) - [N22000397]	1,013.45	12/2021	0.01
25	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO(SOUTH EASTERN RAILWAY) - [N22000398]	524.43	12/2021	184.33
	<u>August,2020</u>			
	<u>SHIPPING AND PORTS</u>			
26	SETHUSAMUDRAM SHIP CHANNEL PROJECT (PORT TRUST) - [250100175]	2,427.40	10/2008	0.00
27	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) (PORT TRUST) - [N25000035]	150.00	03/2006	0.00
28	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB(MUMBAI PORT TRUST) - [N25000063]	366.39	12/2010	0.00
29	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED (KAMARAJAR PORT LIMITED) - [N25000066]	244.50	12/2017	0.00
30	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT (KAMARAJAR PORT LIMITED) - [N25000070]	600.00	12/2017	0.00
31	NEW LARGE DRY DOCK AT COCHIN SHIPYARD LIMITED PREMISES AT KOCHI KERALA (COCHIN SHIPYARD LTD) - [N25000073]	1,799.00	05/2021	347.03
32	INTERNATIONAL SHIP REPAIR FACILITY PROJECT AT COCHIN PORT TRUST PREMISES (COCHIN SHIPYARD LTD) - [N25000074]	970.00	05/2020	322.54
	<u>DEFENCE PRODUCTION</u>			
33	CONSTRUCTION WORKS PHASE 4 (GOA SHIPYARD LIMITED) - [N39000001]	167.69	05/2018	141.83
34	CONSTRUCTION WORKS PHASE 3B (GOA SHIPYARD LIMITED) - [N39000002]	285.95	08/2020	84.40

Month wise List of Deleted Projects Costing Rs. 150 crore and above during

2019-2020

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	October,2020			
	<u>RAILWAYS</u>			
35	CONSTRUCTION OF ROBS IN THE STATE OF BIHAR (NEW ROBS-12) (SOUTH EASTERN RAILWAY) - [N22000337]	400.00	03/2014	0.00
36	CONSTRUCTION OF ROBS IN THE STATE OF BIHAR (EAST CENTRAL RAILWAYS) - [N22000344]	599.63	12/2007	0.00
	December,2020			
	<u>INFORMATION AND BROADCASTING</u>			
37	NATIONAL FILM HERITAGE MISSION (National Film Archive of India) - [N09000001]	597.41	-	29.80
38	FILM AND TELEVISION INSTITUTE ARUNACHAL PRADESH (CENTRAL PUBLIC WORKS DEPARTMENT) - [N09000002]	204.32	02/2019	0.00
39	NATIONAL CENTRE OF EXCELLENCE FOR ANIMATION VISUAL EFFECTS GAMING AND COMICS (NATIONAL BUILDING CONSTRUCION CORPORATION LTD) - [N09000003]	167.70	03/2020	0.00
	January,2020			
	<u>PETROLEUM</u>			
40	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000311]	300.00	04/2021	1.09

TABLE-4

Projects Added / Completed / Dropped / Frozen Rs. 150 Crore and above

No of Projects in Previous Month	1701
No of Projects Completed/Dropped/Frozen in Current Month	13
No of Projects Fell Down in Current Month	1
No of Projects added in Current Month	5
No of Projects in Current Month	1692

Project status Rs. 150 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	552 (32.62%)	14 (.83%)	302 (17.85%)	158 (9.34%)	666 (39.36%)	1692
Latest Approved (Date)	451 (26.65%)	22 (1.30%)	428 (25.30%)	120 (7.09%)	671 (39.66%)	1692

Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	1290	16,00,310.58	17,54,418.85	6,99,856.48	39.90	1,54,108.27	9.60
Project with Revision in Cost	402	7,26,596.82	7,23,597.60	3,97,748.16	55.00	-2,999.22	-.40
Total	1,692	23,26,907.40	24,78,016.45	10,97,604.64	44.29	1,51,109.05	6.49
Original Cost of All Projects							
Original Cost	1,692	20,75,212.70	24,78,016.45	10,97,604.64	44.29	4,02,803.75	19.41

Delayed Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	552	9,24,314.68	11,94,244.91	6,62,402.75	55.50	2,69,930.23	29.20
Latest Approved (RCE)	451	8,28,176.50	9,01,066.51	4,56,961.53	50.70	72,890.01	8.80
Additional Delayed Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Latest Approved	101	1,62,735.87	2,30,083.37	1,60,055.40	69.60	67,347.50	41.40

TABLE-5

Extent of cost overrun in projects with respect to original schedule(Sector Wise)						Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)			
						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	48.51
2	CIVIL AVIATION	13	8,607.51	8,734.44	1.47	3	1,513.40	1,640.33	8.39
3	COAL	107	1,04,637.11	1,08,558.02	3.75	12	28,387.67	33,184.03	16.90
4	FERTILISERS	4	1,101.28	1,101.28	0.00	0	0.00	0.00	0.00
5	MINES	5	7,078.62	7,075.17	-0.05	0	0.00	0.00	0.00
6	STEEL	9	26,228.23	33,485.23	27.67	1	15,525.00	23,140.00	49.05
7	PETROLEUM	148	2,69,889.88	2,84,938.40	5.58	26	63,973.09	81,125.47	26.81
8	POWER	64	2,73,781.33	3,44,106.51	25.69	26	1,59,920.84	2,30,763.07	44.30
9	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0.00
10	HEALTH AND FAMILY WELFARE	23	12,454.56	12,796.11	2.74	12	5,589.39	6,273.60	12.24
11	RAILWAYS	312	4,59,394.75	6,71,692.95	46.21	191	1,87,179.52	4,10,551.11	119.34
12	ROAD TRANSPORT AND HIGHWAYS	867	5,13,537.42	5,28,085.90	2.83	108	73,726.80	94,589.63	28.30
13	SHIPPING AND PORTS	1	4,200.00	5,369.18	27.84	1	4,200.00	5,369.18	27.84
14	TELECOMMUNICATIONS	4	16,095.23	27,333.53	69.82	2	13,565.80	24,904.10	83.58
15	URBAN DEVELOPMENT	74	2,63,824.96	2,71,185.14	2.79	13	28,403.46	35,885.01	26.34
16	WATER RESOURCES	50	26,999.51	72,397.34	168.14	1	10,151.04	55,548.87	447.22
17	COMMERCE AND INDUSTRY	2	17,352.09	17,757.09	2.33	1	4,773.00	5,178.00	8.49
18	HUMAN RESOURCE DEVELOPMENT	4	1,356.22	1,498.16	10.47	1	484.32	626.26	29.31
Total		1692	20,75,212.70	24,78,016.45	19.41	401	6,24,664.33	10,49,277.66	67.97

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-6

Extent of cost overrun in projects with respect to original schedule(State Wise) Rs. 150						Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with cost overrun^			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	74	1,18,849.80	1,74,097.08	46.49	14	45,574.33	1,01,661.32	123.07
2	ARUNACHAL PRADESH	40	21,795.08	40,754.39	86.99	5	9,284.82	28,244.13	204.20
3	ASSAM	46	45,966.37	50,592.00	10.06	17	6,367.74	11,307.37	77.57
4	BIHAR	104	92,846.83	1,28,093.38	37.96	32	39,704.06	75,835.80	91.00
5	GOA	11	5,629.77	5,640.26	0.19	2	529.17	539.66	1.98
6	GUJARAT	59	87,567.29	93,803.49	7.12	10	17,947.78	24,999.36	39.29
7	HARYANA	43	34,582.59	38,034.22	9.98	7	4,921.98	8,784.09	78.47
8	HIMACHAL PRADESH	13	18,162.17	28,392.70	56.33	3	8,237.58	18,468.11	124.19
9	JAMMU AND KASHMIR	16	20,520.64	46,447.89	126.35	3	6,236.00	32,296.00	417.90
10	KARNATAKA	64	73,464.28	77,159.37	5.03	15	13,979.23	18,026.74	28.95
11	KERALA	20	36,309.60	40,285.87	10.95	9	16,705.01	20,876.82	24.97
12	MADHYA PRADESH	80	87,338.98	95,538.30	9.39	14	31,800.23	41,005.41	28.95
13	MAHARASHTRA	252	2,33,558.29	2,44,633.94	4.74	33	40,991.72	57,421.33	40.08
14	MANIPUR	5	6,002.36	14,012.39	133.45	1	4,454.17	12,524.00	181.17
15	MEGHALAYA	7	3,245.09	8,481.17	161.35	2	1,390.78	6,626.86	376.49
16	MIZORAM	13	7,757.62	11,189.69	44.24	5	3,593.57	7,025.64	95.51
17	NAGALAND	26	14,842.43	17,765.36	19.69	2	2,699.59	6,193.81	129.44
18	ODISHA	91	1,04,396.42	1,06,834.86	2.34	16	26,552.73	32,570.70	22.66
19	PUNJAB	27	13,539.35	15,632.85	15.46	8	4,519.58	6,855.53	51.69
20	RAJASTHAN	61	45,605.93	53,170.39	16.59	14	19,109.85	26,674.31	39.58
21	SIKKIM	9	3,476.73	6,368.17	83.17	3	1,909.76	4,801.20	151.40
22	TAMIL NADU	64	1,14,330.18	1,32,336.42	15.75	22	38,120.39	57,727.70	51.44
23	TRIPURA	7	1,977.29	2,159.55	9.22	5	1,436.39	1,618.65	12.69
24	UTTAR PRADESH	132	1,51,011.30	1,57,228.23	4.12	22	51,042.28	59,378.44	16.33
25	WEST BENGAL	77	62,203.95	79,188.60	27.30	25	27,245.03	44,565.97	63.57
26	A & N ISLANDS	9	2,786.01	2,893.59	3.86	2	552.41	679.33	22.98
27	CHANDIGARH	2	349.15	570.00	63.25	2	349.15	570.00	63.25
28	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	0.00
29	DELHI	34	89,958.97	91,744.92	1.99	8	11,481.62	13,346.77	16.24
30	PONDICHERRY	1	195.00	195.00	0.00	0	0.00	0.00	0.00
31	CHHATISGARH	43	77,690.97	89,413.27	15.09	9	35,322.59	47,475.45	34.41
32	JHARKHAND	48	62,232.07	67,540.06	8.53	9	23,217.46	28,529.23	22.88
33	UTTARAKHAND	32	34,435.70	39,959.77	16.04	8	8,540.17	14,090.74	64.99
34	TELANGANA	55	39,236.69	41,702.69	6.28	10	5,264.17	8,383.44	59.25
35	MULTI STATE	126	3,57,261.72	4,70,314.27	31.64	64	1,15,582.99	2,30,173.75	99.14

Extent of cost overrun in projects with respect to original schedule(State Wise) Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun^			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
Total		1692	20,75,212.70	24,78,016.45	19.41	401	6,24,664.33	10,49,277.66	67.97

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-7

Extent of time overrun in projects with respect to original schedule Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	4	67,120.00	80,348.00	36 - 133
2	CIVIL AVIATION	13	8,607.51	8,734.44	1.47	4	3,234.90	3,361.62	6 - 21
3	COAL	107	1,04,637.11	1,08,558.02	3.75	39	22,430.74	26,878.22	12 - 144
4	FERTILISERS	4	1,101.28	1,101.28	0.00	2	458.64	458.64	6 - 6
5	MINES	5	7,078.62	7,075.17	-0.05	2	5,706.62	5,703.17	18 - 20
6	STEEL	9	26,228.23	33,485.23	27.67	8	25,964.87	33,221.87	17 - 62
7	PETROLEUM	148	2,69,889.88	2,84,938.40	5.58	60	1,41,663.58	1,53,133.06	1 - 110
8	POWER	64	2,73,781.33	3,44,106.51	25.69	48	2,03,414.11	2,73,668.23	1 - 155
9	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	1	1,554.00	1,554.00	6 - 6
10	HEALTH AND FAMILY WELFARE	23	12,454.56	12,796.11	2.74	11	4,693.67	4,558.36	4 - 82
11	RAILWAYS	312	4,59,394.75	6,71,692.95	46.21	148	1,85,926.71	2,81,911.53	1 - 324
12	ROAD TRANSPORT AND HIGHWAYS	867	5,13,537.42	5,28,085.90	2.83	186	1,26,706.35	1,34,321.29	1 - 149
13	SHIPPING AND PORTS	1	4,200.00	5,369.18	27.84	0	0.00	0.00	-
14	TELECOMMUNICATIONS	4	16,095.23	27,333.53	69.82	2	13,565.80	24,904.10	16 - 58
15	URBAN DEVELOPMENT	74	2,63,824.96	2,71,185.14	2.79	29	92,897.89	95,301.25	3 - 89
16	WATER RESOURCES	50	26,999.51	72,397.34	168.14	5	11,140.39	56,538.22	2 - 21
17	COMMERCE AND INDUSTRY	2	17,352.09	17,757.09	2.33	2	17,352.09	17,757.09	9 - 12
18	HUMAN RESOURCE DEVELOPMENT	4	1,356.22	1,498.16	10.47	1	484.32	626.26	75 - 75
Total		1692	20,75,212.70	24,78,016.45	19.41	552	9,24,314.68	11,94,244.91	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-8

Extent of time overrun in projects with respect to original schedule(State Wise)						Rs.	150	Crore and above	
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	74	1,18,849.80	1,74,097.08	46.49	37	92,682.99	1,46,857.92	1 - 168
2	ARUNACHAL PRADESH	40	21,795.08	40,754.39	86.99	10	11,585.23	30,242.75	21 - 155
3	ASSAM	46	45,966.37	50,592.00	10.06	14	9,005.05	10,528.98	2 - 149
4	BIHAR	104	92,846.83	1,28,093.38	37.96	21	38,931.25	64,002.02	7 - 118
5	GOA	11	5,629.77	5,640.26	0.19	0	0.00	0.00	-
6	GUJARAT	59	87,567.29	93,803.49	7.12	16	35,425.12	41,704.45	3 - 120
7	HARYANA	43	34,582.59	38,034.22	9.98	11	8,252.59	10,575.09	1 - 118
8	HIMACHAL PRADESH	13	18,162.17	28,392.70	56.33	3	7,339.98	13,417.50	15 - 147
9	JAMMU AND KASHMIR	16	20,520.64	46,447.89	126.35	5	9,893.33	35,342.33	18 - 235
10	KARNATAKA	64	73,464.28	77,159.37	5.03	23	48,626.17	50,314.54	3 - 264
11	KERALA	20	36,309.60	40,285.87	10.95	8	16,439.68	18,613.55	8 - 89
12	MADHYA PRADESH	80	87,338.98	95,538.30	9.39	38	45,496.54	52,877.68	1 - 73
13	MAHARASHTRA	252	2,33,558.29	2,44,633.94	4.74	65	1,03,981.33	1,09,022.44	1 - 204
14	MANIPUR	5	6,002.36	14,012.39	133.45	3	5,188.43	13,198.46	36 - 132
15	MEGHALAYA	7	3,245.09	8,481.17	161.35	2	848.31	990.25	26 - 75
16	MIZORAM	13	7,757.62	11,189.69	44.24	5	3,593.57	7,025.64	69 - 128
17	NAGALAND	26	14,842.43	17,765.36	19.69	5	3,912.63	7,260.36	23 - 79
18	ODISHA	91	1,04,396.42	1,06,834.86	2.34	35	54,167.45	56,605.20	3 - 183
19	PUNJAB	27	13,539.35	15,632.85	15.46	12	6,256.92	7,752.92	4 - 34
20	RAJASTHAN	61	45,605.93	53,170.39	16.59	12	17,794.39	23,400.43	1 - 75
21	SIKKIM	9	3,476.73	6,368.17	83.17	0	0.00	0.00	-
22	TAMIL NADU	64	1,14,330.18	1,32,336.42	15.75	27	74,649.75	83,186.15	4 - 133
23	TRIPURA	7	1,977.29	2,159.55	9.22	1	569.63	670.00	18 - 18
24	UTTAR PRADESH	132	1,51,011.30	1,57,228.23	4.12	34	45,027.91	48,453.31	2 - 66
25	WEST BENGAL	77	62,203.95	79,188.60	27.30	27	32,802.07	44,692.50	2 - 324
26	A & N ISLANDS	9	2,786.01	2,893.59	3.86	1	314.61	441.33	21 - 21
27	CHANDIGARH	2	349.15	570.00	63.25	0	0.00	0.00	-
28	D & N HAVELI	1	6,086.08	5,842.31	-4.01	1	6,086.08	5,842.31	10 - 10
29	DELHI	34	89,958.97	91,744.92	1.99	12	15,067.74	16,892.29	6 - 82
30	PONDICHERRY	1	195.00	195.00	0.00	1	195.00	195.00	4 - 4
31	CHHATISGARH	43	77,690.97	89,413.27	15.09	14	40,094.59	51,518.00	3 - 84
32	JHARKHAND	48	62,232.07	67,540.06	8.53	18	23,203.33	24,598.55	9 - 120
33	UTTARAKHAND	32	34,435.70	39,959.77	16.04	7	23,203.88	28,115.11	3 - 114
34	TELANGANA	55	39,236.69	41,702.69	6.28	22	19,784.22	20,172.97	9 - 156
35	MULTI STATE	126	3,57,261.72	4,70,314.27	31.64	62	1,23,894.91	1,69,734.88	3 - 252
Total		1692	20,75,212.70	24,78,016.45	19.41	552	9,24,314.68	11,94,244.91	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-9

<u>Extent of time overrun in projects with respect to latest schedule</u>						Rs. 150 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	69,305.00	80,348.00	15.93	4	69,305.00	80,348.00	36 - 133
2	CIVIL AVIATION	13	8,607.51	8,734.44	1.47	4	3,234.90	3,361.62	6 - 21
3	COAL	107	1,05,368.36	1,08,558.02	3.03	39	34,310.47	37,277.59	0 - 144
4	FERTILISERS	4	1,101.28	1,101.28	0.00	2	458.64	458.64	6 - 6
5	MINES	5	7,075.17	7,075.17	0.00	0	0.00	0.00	-
6	STEEL	9	33,843.23	33,485.23	-1.06	2	1,417.05	1,417.05	17 - 27
7	PETROLEUM	148	2,83,851.38	2,84,938.40	0.38	39	81,049.39	81,060.60	1 - 56
8	POWER	64	3,06,300.66	3,44,106.51	12.34	32	1,28,531.82	1,42,431.54	1 - 114
9	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	1	1,554.00	1,554.00	6 - 6
10	HEALTH AND FAMILY WELFARE	23	12,574.56	12,796.11	1.76	11	4,693.67	4,558.36	4 - 82
11	RAILWAYS	312	5,82,961.69	6,71,692.95	15.22	123	2,07,065.70	2,44,385.42	1 - 264
12	ROAD TRANSPORT AND HIGHWAYS	867	5,36,239.81	5,28,085.90	-1.52	165	1,32,086.22	1,26,563.16	0 - 149
13	SHIPPING AND PORTS	1	5,369.18	5,369.18	0.00	0	0.00	0.00	-
14	TELECOMMUNICATIONS	4	16,103.53	27,333.53	69.74	1	13,334.00	24,664.00	58 - 58
15	URBAN DEVELOPMENT	74	2,65,486.30	2,71,185.14	2.15	24	77,750.36	79,054.31	0 - 89
16	WATER RESOURCES	50	72,457.43	72,397.34	-0.08	1	55,548.87	55,548.87	21 - 21
17	COMMERCE AND INDUSTRY	2	17,352.09	17,757.09	2.33	2	17,352.09	17,757.09	9 - 12
18	HUMAN RESOURCE DEVELOPMENT	4	1,356.22	1,498.16	10.47	1	484.32	626.26	75 - 75
Total		1692	23,26,907.40	24,78,016.45	6.49	451	8,28,176.50	9,01,066.51	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-10

<u>Extent of cost overrun in projects with respect to latest schedule</u>						Rs. 150 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	69,305.00	80,348.00	15.93	3	29,456.00	40,499.00	37.49
2	CIVIL AVIATION	13	8,607.51	8,734.44	1.47	3	1,513.40	1,640.33	8.39
3	COAL	107	1,05,368.36	1,08,558.02	3.03	10	22,328.13	25,644.13	14.85
4	FERTILISERS	4	1,101.28	1,101.28	0.00	0	0.00	0.00	0.00
5	MINES	5	7,075.17	7,075.17	0.00	0	0.00	0.00	0.00
6	STEEL	9	33,843.23	33,485.23	-1.06	0	0.00	0.00	0.00
7	PETROLEUM	148	2,83,851.38	2,84,938.40	0.38	11	13,421.19	16,327.56	21.66
8	POWER	64	3,06,300.66	3,44,106.51	12.34	16	1,16,901.04	1,55,223.94	32.78
9	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0.00
10	HEALTH AND FAMILY WELFARE	23	12,574.56	12,796.11	1.76	11	4,238.39	4,802.60	13.31
11	RAILWAYS	312	5,82,961.69	6,71,692.95	15.22	145	1,31,610.71	2,34,600.00	78.25
12	ROAD TRANSPORT AND HIGHWAYS	867	5,36,239.81	5,28,085.90	-1.52	119	75,575.45	89,381.14	18.27
13	SHIPPING AND PORTS	1	5,369.18	5,369.18	0.00	0	0.00	0.00	0.00
14	TELECOMMUNICATIONS	4	16,103.53	27,333.53	69.74	1	13,334.00	24,664.00	84.97
15	URBAN DEVELOPMENT	74	2,65,486.30	2,71,185.14	2.15	6	23,246.97	29,064.41	25.02
16	WATER RESOURCES	50	72,457.43	72,397.34	-0.08	0	0.00	0.00	0.00
17	COMMERCE AND INDUSTRY	2	17,352.09	17,757.09	2.33	1	4,773.00	5,178.00	8.49
18	HUMAN RESOURCE DEVELOPMENT	4	1,356.22	1,498.16	10.47	1	484.32	626.26	29.31
Total		1692	23,26,907.40	24,78,016.45	6.49	327	4,36,882.60	6,27,651.37	43.67

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-11

Extent of time & cost overrun in projects with respect to latest schedule						Rs. 150	Crore and above		
(All Cost/ Expenditure in Rs. crore)						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	69,305.00	80,348.00	15.93	3	29,456.00	40,499.00	69- 133
2	CIVIL AVIATION	13	8,607.51	8,734.44	1.47	1	314.61	441.33	21- 21
3	COAL	107	1,05,368.36	1,08,558.02	3.03	8	4,903.19	7,996.65	12- 144
4	FERTILISERS	4	1,101.28	1,101.28	0.00	0	0.00	0.00	0- 0
5	MINES	5	7,075.17	7,075.17	0.00	0	0.00	0.00	0- 0
6	STEEL	9	33,843.23	33,485.23	-1.06	0	0.00	0.00	0- 0
7	PETROLEUM	148	2,83,851.38	2,84,938.40	0.38	1	543.91	682.90	4- 4
8	POWER	64	3,06,300.66	3,44,106.51	12.34	9	67,695.68	81,595.40	1- 114
9	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0- 0
10	HEALTH AND FAMILY WELFARE	23	12,574.56	12,796.11	1.76	5	1,337.34	1,544.69	12- 82
11	RAILWAYS	312	5,82,961.69	6,71,692.95	15.22	58	61,523.98	1,08,749.79	6- 252
12	ROAD TRANSPORT AND HIGHWAYS	867	5,36,239.81	5,28,085.90	-1.52	23	19,422.60	24,570.43	2- 143
13	SHIPPING AND PORTS	1	5,369.18	5,369.18	0.00	0	0.00	0.00	0- 0
14	TELECOMMUNICATIONS	4	16,103.53	27,333.53	69.74	1	13,334.00	24,664.00	58- 58
15	URBAN DEVELOPMENT	74	2,65,486.30	2,71,185.14	2.15	3	7,403.00	8,717.13	17- 45
16	WATER RESOURCES	50	72,457.43	72,397.34	-0.08	0	0.00	0.00	0- 0
17	COMMERCE AND INDUSTRY	2	17,352.09	17,757.09	2.33	1	4,773.00	5,178.00	9- 9
18	HUMAN RESOURCE DEVELOPMENT	4	1,356.22	1,498.16	10.47	1	484.32	626.26	75- 75
Total		1692	23,26,907.40	24,78,016.45	6.49	114	2,11,191.63	3,05,265.58	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-12

Extent of time & cost overrun in projects with respect to original schedule						Rs. 150 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	69- 133
2	CIVIL AVIATION	13	8,607.51	8,734.44	1.47	1	314.61	441.33	21- 21
3	COAL	107	1,04,637.11	1,08,558.02	3.75	10	10,962.73	15,536.55	12- 144
4	FERTILISERS	4	1,101.28	1,101.28	0.00	0	0.00	0.00	0- 0
5	MINES	5	7,078.62	7,075.17	-0.05	0	0.00	0.00	0- 0
6	STEEL	9	26,228.23	33,485.23	27.67	1	15,525.00	23,140.00	62- 62
7	PETROLEUM	148	2,69,889.88	2,84,938.40	5.58	15	50,537.56	63,174.50	1- 110
8	POWER	64	2,73,781.33	3,44,106.51	25.69	24	1,54,155.88	2,24,410.00	1- 155
9	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0- 0
10	HEALTH AND FAMILY WELFARE	23	12,454.56	12,796.11	2.74	5	1,337.34	1,544.69	12- 82
11	RAILWAYS	312	4,59,394.75	6,71,692.95	46.21	93	97,898.67	2,02,840.94	3- 324
12	ROAD TRANSPORT AND HIGHWAYS	867	5,13,537.42	5,28,085.90	2.83	37	29,726.55	39,165.80	1- 143
13	SHIPPING AND PORTS	1	4,200.00	5,369.18	27.84	0	0.00	0.00	0- 0
14	TELECOMMUNICATIONS	4	16,095.23	27,333.53	69.82	2	13,565.80	24,904.10	16- 58
15	URBAN DEVELOPMENT	74	2,63,824.96	2,71,185.14	2.79	7	12,392.49	14,838.02	6- 45
16	WATER RESOURCES	50	26,999.51	72,397.34	168.14	1	10,151.04	55,548.87	21- 21
17	COMMERCE AND INDUSTRY	2	17,352.09	17,757.09	2.33	1	4,773.00	5,178.00	9- 9
18	HUMAN RESOURCE DEVELOPMENT	4	1,356.22	1,498.16	10.47	1	484.32	626.26	75- 75
Total		1692	20,75,212.70	24,78,016.45	19.41	201	4,29,095.99	7,11,848.06	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-13

State-Wise Position of Central Sector Projects costing Rs. 150 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	74	1,18,849.80	1,74,097.08	46.49	11	41,830.50	96,708.76	1 - 168
2	ARUNACHAL PRADESH	40	21,795.08	40,754.39	86.99	3	8,921.16	27,578.68	36 - 155
3	ASSAM	46	45,966.37	50,592.00	10.06	4	1,451.11	3,172.90	4 - 143
4	BIHAR	104	92,846.83	1,28,093.38	37.96	11	31,377.45	56,455.93	12 - 118
5	GOA	11	5,629.77	5,640.26	0.19	0	0.00	0.00	-
6	GUJARAT	59	87,567.29	93,803.49	7.12	6	15,438.03	21,873.69	8 - 120
7	HARYANA	43	34,582.59	38,034.22	9.98	2	1,395.00	3,717.50	100 - 111
8	HIMACHAL PRADESH	13	18,162.17	28,392.70	56.33	1	3,919.59	9,997.11	147 - 147
9	JAMMU AND KASHMIR	16	20,520.64	46,447.89	126.35	1	2,500.00	27,949.00	235 - 235
10	KARNATAKA	64	73,464.28	77,159.37	5.03	6	6,128.21	8,130.00	3 - 36
11	KERALA	20	36,309.60	40,285.87	10.95	4	12,006.19	14,204.10	18 - 44
12	MADHYA PRADESH	80	87,338.98	95,538.30	9.39	11	30,036.44	37,514.88	1 - 73
13	MAHARASHTRA	252	2,33,558.29	2,44,633.94	4.74	21	25,111.48	35,307.44	1 - 204
14	MANIPUR	5	6,002.36	14,012.39	133.45	1	4,454.17	12,524.00	132 - 132
15	MEGHALAYA	7	3,245.09	8,481.17	161.35	1	484.32	626.26	75 - 75
16	MIZORAM	13	7,757.62	11,189.69	44.24	5	3,593.57	7,025.64	69 - 128
17	NAGALAND	26	14,842.43	17,765.36	19.69	2	2,699.59	6,193.81	43 - 79
18	ODISHA	91	1,04,396.42	1,06,834.86	2.34	12	23,703.70	29,641.02	12 - 183
19	PUNJAB	27	13,539.35	15,632.85	15.46	6	3,425.12	5,108.81	6 - 34
20	RAJASTHAN	61	45,605.93	53,170.39	16.59	6	13,980.95	19,586.99	12 - 75
21	SIKKIM	9	3,476.73	6,368.17	83.17	0	0.00	0.00	-
22	TAMIL NADU	64	1,14,330.18	1,32,336.42	15.75	7	15,872.04	24,411.89	12 - 133
23	TRIPURA	7	1,977.29	2,159.55	9.22	1	569.63	670.00	18 - 18
24	UTTAR PRADESH	132	1,51,011.30	1,57,228.23	4.12	6	23,329.58	27,362.73	3 - 50
25	WEST BENGAL	77	62,203.95	79,188.60	27.30	12	21,686.74	33,592.20	12 - 324
26	A & N ISLANDS	9	2,786.01	2,893.59	3.86	1	314.61	441.33	21 - 21
27	CHANDIGARH	2	349.15	570.00	63.25	0	0.00	0.00	-
28	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	-
29	DELHI	34	89,958.97	91,744.92	1.99	6	11,168.41	12,992.96	6 - 82
30	PONDICHERRY	1	195.00	195.00	0.00	0	0.00	0.00	-
31	CHHATISGARH	43	77,690.97	89,413.27	15.09	7	33,816.43	45,670.40	3 - 62
32	JHARKHAND	48	62,232.07	67,540.06	8.53	4	16,497.75	17,892.97	9 - 39
33	UTTARAKHAND	32	34,435.70	39,959.77	16.04	3	6,075.90	10,987.64	19 - 114
34	TELANGANA	55	39,236.69	41,702.69	6.28	7	2,427.32	3,469.34	9 - 144
35	MULTI STATE	126	3,57,261.72	4,70,314.27	31.64	33	64,881.00	1,11,040.08	9 - 252
Total		1692	20,75,212.70	24,78,016.45	19.41	201	4,29,095.99	7,11,848.06	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-14

EXECUTIVE SUMMARY COSTING Rs. 1000 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	154	3
2	ROAD TRANSPORT AND HIGHWAYS	152	5
3	PETROLEUM	58	6
4	POWER	39	9
5	URBAN DEVELOPMENT	22	1
6	COAL	16	0
7	STEEL	6	3
8	ATOMIC ENERGY	4	2
9	HEALTH AND FAMILY WELFARE	3	1
10	CIVIL AVIATION	2	0
11	TELECOMMUNICATIONS	2	0
12	COMMERCE AND INDUSTRY	2	0
13	MINES	1	0
14	HEAVY INDUSTRY	1	0
15	SHIPPING AND PORTS	1	0
16	WATER RESOURCES	1	1
	Total	464	31

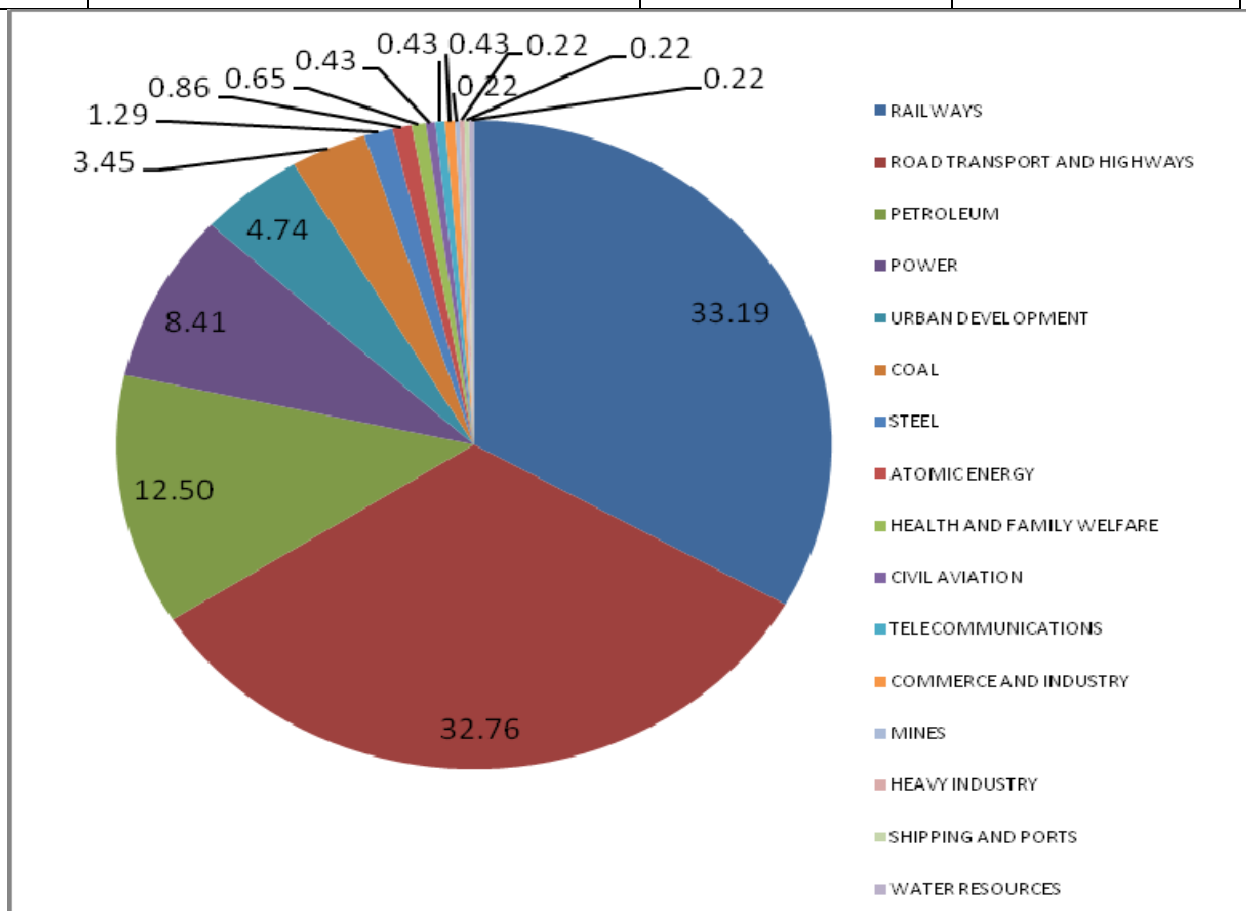


TABLE-15

Projects Added / Completed / Dropped / Frozen Rs. 1000 Crore and above

No of Projects in Previous Month	466
No of Projects Completed/Dropped/Frozen in Current Month	4
No of Projects Fell Down in Current Month	1
No of Projects added in Current Month	3
No of Projects in Current Month	464

Project status Rs. 1000 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	212 (45.69%)	5 (1.08%)	82 (17.67%)	53 (11.42%)	112 (24.14%)	464
Latest Approved (Date)	168 (36.21%)	6 (1.29%)	134 (28.88%)	42 (9.05%)	114 (24.57%)	464

Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	331	12,08,401.78	13,56,017.73	5,31,733.61	39.20	1,47,615.95	12.20
Project with Revision in Cost	133	6,07,711.82	6,09,421.87	3,38,676.41	55.60	1,710.05	.30
Total	464	18,16,113.60	19,65,439.60	8,70,410.02	44.29	1,49,326.00	8.22
Original Cost of All Projects							
Original Cost	464	15,78,418.68	19,65,439.60	8,70,410.02	44.29	3,87,020.92	24.52

Delayed Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	212	7,76,946.74	10,42,361.94	5,79,771.52	55.60	2,65,415.20	34.16
Latest Approved (RCE)	168	6,96,872.16	7,74,749.96	3,89,994.02	50.30	77,877.80	11.18

Additional Delayed Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Latest Approved	31	1,33,164.68	1,99,562.10	1,41,118.19	70.70	66,397.42	49.90
Total	31	1,33,164.68	1,99,562.10	1,41,118.19	70.71	66,397.42	49.86

TABLE-16

Extent of cost overrun in projects with respect to original schedule(Sector Wise) Rs. 1000 Crore and above									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	48.51
2	CIVIL AVIATION	2	3,850.00	3,850.00	0.00	0	0.00	0.00	0.00
3	COAL	16	66,016.48	69,675.33	5.54	3	25,805.84	29,464.69	14.18
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
5	STEEL	6	25,381.34	32,638.34	28.59	1	15,525.00	23,140.00	49.05
6	PETROLEUM	58	2,33,310.53	2,47,837.67	6.23	16	58,721.29	75,185.51	28.04
7	POWER	39	2,63,372.45	3,33,464.84	26.61	23	1,58,707.78	2,29,317.22	44.49
8	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0.00
9	HEALTH AND FAMILY WELFARE	3	4,332.00	4,703.00	8.56	2	2,928.00	3,299.00	12.67
10	RAILWAYS	154	3,91,155.69	5,91,398.09	51.19	101	1,55,626.99	3,61,222.27	132.11
11	ROAD TRANSPORT AND HIGHWAYS	152	2,21,835.53	2,34,280.53	5.61	35	45,388.87	58,862.24	29.68
12	SHIPPING AND PORTS	1	4,200.00	5,369.18	27.84	1	4,200.00	5,369.18	27.84
13	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	84.97
14	URBAN DEVELOPMENT	22	2,47,802.36	2,54,799.49	2.82	5	26,033.88	33,110.21	27.18
15	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	447.22
16	COMMERCE AND INDUSTRY	2	17,352.09	17,757.09	2.33	1	4,773.00	5,178.00	8.49
Total		464	15,78,418.68	19,65,439.60	24.52	193	5,48,466.69	9,44,860.19	72.27

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-17

Extent of cost overrun in projects with respect to original schedule(State Wise) Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun [^]			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	20	97,962.39	1,53,647.17	56.84	10	44,401.22	1,00,444.00	126.22
2	ARUNACHAL PRADESH	5	13,732.92	32,374.37	135.74	2	8,782.23	27,423.68	212.26
3	ASSAM	8	31,807.34	34,497.52	8.46	3	2,127.51	4,868.01	128.81
4	BIHAR	23	57,179.10	90,364.87	58.04	13	31,489.79	64,675.56	105.39
5	GUJARAT	21	69,363.23	74,844.09	7.90	5	16,275.45	22,415.36	37.73
6	HARYANA	15	21,618.98	24,638.36	13.97	3	2,699.20	5,718.58	111.86
7	HIMACHAL PRADESH	7	15,497.19	25,727.72	66.02	3	8,237.58	18,468.11	124.19
8	JAMMU AND KASHMIR	10	18,318.84	44,246.09	141.53	3	6,236.00	32,296.00	417.90
9	KARNATAKA	19	55,423.75	58,845.64	6.17	8	10,837.45	14,275.34	31.72
10	KERALA	9	30,871.86	34,724.00	12.48	6	14,996.96	18,873.14	25.85
11	MADHYA PRADESH	22	60,547.97	68,655.23	13.39	10	30,368.63	38,993.93	28.40
12	MAHARASHTRA	51	1,53,981.12	1,67,689.59	8.90	18	35,388.04	49,935.77	41.11
13	MANIPUR	1	4,454.17	12,524.00	181.17	1	4,454.17	12,524.00	181.17
14	MEGHALAYA	1	906.46	6,000.60	561.98	1	906.46	6,000.60	561.98
15	MIZORAM	1	2,393.47	5,021.45	109.80	1	2,393.47	5,021.45	109.80
16	NAGALAND	3	7,896.52	11,376.81	44.07	1	2,326.52	5,806.81	149.59
17	ODISHA	34	81,194.16	83,178.70	2.44	10	25,048.54	30,532.65	21.89
18	PUNJAB	3	3,627.54	4,826.70	33.06	1	1,388.34	2,587.50	86.37
19	RAJASTHAN	10	22,632.33	28,820.49	27.34	4	15,115.90	21,304.06	40.94
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	204.95
21	TAMIL NADU	24	95,454.89	1,11,375.19	16.68	12	34,925.92	51,543.22	47.58
22	UTTAR PRADESH	43	1,12,731.46	1,18,937.71	5.51	12	46,866.04	54,013.42	15.25
23	WEST BENGAL	24	43,267.91	59,223.65	36.88	12	22,816.12	38,802.89	70.07
24	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	0.00
25	DELHI	10	81,740.38	83,303.70	1.91	3	10,256.21	11,898.73	16.01
26	CHHATISGARH	14	65,083.62	76,559.60	17.63	7	34,693.96	46,471.96	33.95
27	JHARKHAND	13	49,100.48	53,989.92	9.96	5	21,821.72	26,711.16	22.41
28	UTTARAKHAND	6	26,039.84	31,109.03	19.47	3	6,997.06	12,066.25	72.45
29	TELANGANA	5	18,567.06	20,644.30	11.19	2	2,378.60	4,455.84	87.33
30	MULTI STATE	60	3,29,598.14	4,38,366.10	33.00	33	1,02,898.12	2,12,647.48	106.66
Total		464	15,78,418.68	19,65,439.60	24.52	193	5,48,466.69	9,44,860.19	72.27

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-18

Extent of time overrun in projects with respect to original schedule Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	4	67,120.00	80,348.00	36 - 133
2	CIVIL AVIATION	2	3,850.00	3,850.00	0.00	1	2,467.00	2,467.00	6 - 6
3	COAL	16	66,016.48	69,675.33	5.54	4	10,854.16	14,512.21	31 - 84
4	MINES	1	5,540.00	5,540.00	0.00	1	5,540.00	5,540.00	20 - 20
5	STEEL	6	25,381.34	32,638.34	28.59	6	25,381.34	32,638.34	17 - 62
6	PETROLEUM	58	2,33,310.53	2,47,837.67	6.23	25	1,25,242.72	1,36,555.71	1 - 110
7	POWER	39	2,63,372.45	3,33,464.84	26.61	29	1,95,811.17	2,65,832.50	1 - 155
8	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	1	1,554.00	1,554.00	6 - 6
9	HEALTH AND FAMILY WELFARE	3	4,332.00	4,703.00	8.56	0	0.00	0.00	-
10	RAILWAYS	154	3,91,155.69	5,91,398.09	51.19	87	1,54,390.14	2,47,606.65	3 - 324
11	ROAD TRANSPORT AND HIGHWAYS	152	2,21,835.53	2,34,280.53	5.61	42	61,579.94	68,894.56	1 - 100
12	SHIPPING AND PORTS	1	4,200.00	5,369.18	27.84	0	0.00	0.00	-
13	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58 - 58
14	URBAN DEVELOPMENT	22	2,47,802.36	2,54,799.49	2.82	8	86,169.14	88,443.01	4 - 64
15	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	21 - 21
16	COMMERCE AND INDUSTRY	2	17,352.09	17,757.09	2.33	2	17,352.09	17,757.09	9 - 12
Total		464	15,78,418.68	19,65,439.60	24.52	212	7,76,946.74	10,42,361.94	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-19

<u>Extent of time overrun in projects with respect to original schedule(State Wise)</u>						Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)			
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	20	97,962.39	1,53,647.17	56.84	12	83,026.60	1,37,523.33	1 - 168
2	ARUNACHAL PRADESH	5	13,732.92	32,374.37	135.74	3	10,035.33	28,676.78	60 - 155
3	ASSAM	8	31,807.34	34,497.52	8.46	3	4,189.20	5,336.00	3 - 12
4	BIHAR	23	57,179.10	90,364.87	58.04	9	32,035.52	56,487.05	12 - 118
5	GUJARAT	21	69,363.23	74,844.09	7.90	7	30,986.43	36,622.85	3 - 69
6	HARYANA	15	21,618.98	24,638.36	13.97	2	4,637.00	6,496.50	7 - 100
7	HIMACHAL PRADESH	7	15,497.19	25,727.72	66.02	2	6,405.52	12,483.04	15 - 147
8	JAMMU AND KASHMIR	10	18,318.84	44,246.09	141.53	5	9,893.33	35,342.33	18 - 235
9	KARNATAKA	19	55,423.75	58,845.64	6.17	11	41,542.14	43,242.71	3 - 264
10	KERALA	9	30,871.86	34,724.00	12.48	5	15,319.19	17,493.06	8 - 44
11	MADHYA PRADESH	22	60,547.97	68,655.23	13.39	11	34,657.85	41,705.42	1 - 73
12	MAHARASHTRA	51	1,53,981.12	1,67,689.59	8.90	25	81,492.06	89,818.34	1 - 204
13	MANIPUR	1	4,454.17	12,524.00	181.17	1	4,454.17	12,524.00	132 - 132
14	MEGHALAYA	1	906.46	6,000.60	561.98	0	0.00	0.00	-
15	MIZORAM	1	2,393.47	5,021.45	109.80	1	2,393.47	5,021.45	96 - 96
16	NAGALAND	3	7,896.52	11,376.81	44.07	1	2,326.52	5,806.81	79 - 79
17	ODISHA	34	81,194.16	83,178.70	2.44	18	47,260.08	49,244.61	12 - 183
18	PUNJAB	3	3,627.54	4,826.70	33.06	2	2,457.93	3,657.09	6 - 14
19	RAJASTHAN	10	22,632.33	28,820.49	27.34	1	12,320.00	17,079.00	75 - 75
20	SIKKIM	1	1,339.48	4,084.69	204.95	0	0.00	0.00	-
21	TAMIL NADU	24	95,454.89	1,11,375.19	16.68	13	68,546.04	76,365.46	4 - 133
22	UTTAR PRADESH	43	1,12,731.46	1,18,937.71	5.51	13	35,752.58	39,636.37	2 - 40
23	WEST BENGAL	24	43,267.91	59,223.65	36.88	14	28,563.46	40,057.03	5 - 324
24	D & N HAVELI	1	6,086.08	5,842.31	-4.01	1	6,086.08	5,842.31	10 - 10
25	DELHI	10	81,740.38	83,303.70	1.91	5	13,204.73	14,847.25	6 - 34
26	CHHATISGARH	14	65,083.62	76,559.60	17.63	8	38,121.02	49,365.91	3 - 62
27	JHARKHAND	13	49,100.48	53,989.92	9.96	5	19,509.24	20,575.75	9 - 84
28	UTTARAKHAND	6	26,039.84	31,109.03	19.47	3	21,686.06	26,481.18	3 - 114
29	TELANGANA	5	18,567.06	20,644.30	11.19	2	11,759.46	11,759.46	10 - 156
30	MULTI STATE	60	3,29,598.14	4,38,366.10	33.00	29	1,08,285.73	1,52,870.85	4 - 252
Total		464	15,78,418.68	19,65,439.60	24.52	212	7,76,946.74	10,42,361.94	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-20

<u>Extent of time overrun in projects with respect to latest schedule</u>						Rs. 1000 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	69,305.00	80,348.00	15.93	4	69,305.00	80,348.00	36 - 133
2	CIVIL AVIATION	2	3,850.00	3,850.00	0.00	1	2,467.00	2,467.00	6 - 6
3	COAL	16	67,189.78	69,675.33	3.70	4	22,613.59	25,098.34	0 - 60
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	-
5	STEEL	6	32,996.34	32,638.34	-1.09	1	1,154.18	1,154.18	27 - 27
6	PETROLEUM	58	2,47,131.43	2,47,837.67	0.29	12	68,833.09	68,833.09	1 - 26
7	POWER	39	2,95,658.99	3,33,464.84	12.79	20	1,23,394.76	1,37,294.48	1 - 114
8	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	1	1,554.00	1,554.00	6 - 6
9	HEALTH AND FAMILY WELFARE	3	4,452.00	4,703.00	5.64	0	0.00	0.00	-
10	RAILWAYS	154	5,08,918.14	5,91,398.09	16.21	71	1,78,125.58	2,16,014.71	3 - 264
11	ROAD TRANSPORT AND HIGHWAYS	152	2,36,735.43	2,34,280.53	-1.04	44	71,248.13	70,763.19	0 - 100
12	SHIPPING AND PORTS	1	5,369.18	5,369.18	0.00	0	0.00	0.00	-
13	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58 - 58
14	URBAN DEVELOPMENT	22	2,49,067.18	2,54,799.49	2.30	6	71,941.87	73,253.01	6 - 64
15	WATER RESOURCES	1	55,548.87	55,548.87	0.00	1	55,548.87	55,548.87	21 - 21
16	COMMERCE AND INDUSTRY	2	17,352.09	17,757.09	2.33	2	17,352.09	17,757.09	9 - 12
Total		464	18,16,113.60	19,65,439.60	8.22	168	6,96,872.16	7,74,749.96	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-21

Extent of cost overrun in projects with respect to latest schedule						Rs. 1000 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with cost overruns [^]			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	69,305.00	80,348.00	15.93	3	29,456.00	40,499.00	37.49
2	CIVIL AVIATION	2	3,850.00	3,850.00	0.00	0	0.00	0.00	0.00
3	COAL	16	67,189.78	69,675.33	3.70	2	19,898.73	22,384.28	12.49
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
5	STEEL	6	32,996.34	32,638.34	-1.09	0	0.00	0.00	0.00
6	PETROLEUM	58	2,47,131.43	2,47,837.67	0.29	5	9,923.66	12,299.17	23.94
7	POWER	39	2,95,658.99	3,33,464.84	12.79	16	1,16,901.04	1,55,223.94	32.78
8	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0.00
9	HEALTH AND FAMILY WELFARE	3	4,452.00	4,703.00	5.64	1	1,577.00	1,828.00	15.92
10	RAILWAYS	154	5,08,918.14	5,91,398.09	16.21	73	1,05,356.57	1,96,694.40	86.69
11	ROAD TRANSPORT AND HIGHWAYS	152	2,36,735.43	2,34,280.53	-1.04	30	40,851.21	49,519.30	21.22
12	SHIPPING AND PORTS	1	5,369.18	5,369.18	0.00	0	0.00	0.00	0.00
13	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	84.97
14	URBAN DEVELOPMENT	22	2,49,067.18	2,54,799.49	2.30	4	22,577.97	28,389.48	25.74
15	WATER RESOURCES	1	55,548.87	55,548.87	0.00	0	0.00	0.00	0.00
16	COMMERCE AND INDUSTRY	2	17,352.09	17,757.09	2.33	1	4,773.00	5,178.00	8.49
	Total	464	18,16,113.60	19,65,439.60	8.22	136	3,64,649.18	5,36,679.57	47.18

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-22

Extent of time & cost overrun in projects with respect to latest schedule						Rs. 1000 Crore and above			
(All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	69,305.00	80,348.00	15.93	3	29,456.00	40,499.00	69- 133
2	CIVIL AVIATION	2	3,850.00	3,850.00	0.00	0	0.00	0.00	0- 0
3	COAL	16	67,189.78	69,675.33	3.70	1	2,661.73	5,146.48	60- 60
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
5	STEEL	6	32,996.34	32,638.34	-1.09	0	0.00	0.00	0- 0
6	PETROLEUM	58	2,47,131.43	2,47,837.67	0.29	0	0.00	0.00	0- 0
7	POWER	39	2,95,658.99	3,33,464.84	12.79	9	67,695.68	81,595.40	1- 114
8	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0- 0
9	HEALTH AND FAMILY WELFARE	3	4,452.00	4,703.00	5.64	0	0.00	0.00	0- 0
10	RAILWAYS	154	5,08,918.14	5,91,398.09	16.21	31	50,122.32	93,263.07	6- 252
11	ROAD TRANSPORT AND HIGHWAYS	152	2,36,735.43	2,34,280.53	-1.04	14	15,203.04	19,624.10	2- 62
12	SHIPPING AND PORTS	1	5,369.18	5,369.18	0.00	0	0.00	0.00	0- 0
13	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58- 58
14	URBAN DEVELOPMENT	22	2,49,067.18	2,54,799.49	2.30	2	6,907.00	8,218.14	17- 32
15	WATER RESOURCES	1	55,548.87	55,548.87	0.00	0	0.00	0.00	0- 0
16	COMMERCE AND INDUSTRY	2	17,352.09	17,757.09	2.33	1	4,773.00	5,178.00	9- 9
Total		464	18,16,113.60	19,65,439.60	8.22	62	1,90,152.77	2,78,188.19	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-23

Extent of time & cost overrun in projects with respect to original schedule						Rs. 1000 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	69- 133
2	CIVIL AVIATION	2	3,850.00	3,850.00	0.00	0	0.00	0.00	0- 0
3	COAL	16	66,016.48	69,675.33	5.54	2	8,568.84	12,226.89	51- 60
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
5	STEEL	6	25,381.34	32,638.34	28.59	1	15,525.00	23,140.00	62- 62
6	PETROLEUM	58	2,33,310.53	2,47,837.67	6.23	11	48,513.94	60,866.61	1- 110
7	POWER	39	2,63,372.45	3,33,464.84	26.61	21	1,52,942.82	2,22,964.15	1- 155
8	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0- 0
9	HEALTH AND FAMILY WELFARE	3	4,332.00	4,703.00	8.56	0	0.00	0.00	0- 0
10	RAILWAYS	154	3,91,155.69	5,91,398.09	51.19	56	83,673.70	1,80,872.83	3- 324
11	ROAD TRANSPORT AND HIGHWAYS	152	2,21,835.53	2,34,280.53	5.61	18	22,525.99	29,840.61	1- 100
12	SHIPPING AND PORTS	1	4,200.00	5,369.18	27.84	0	0.00	0.00	0- 0
13	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58- 58
14	URBAN DEVELOPMENT	22	2,47,802.36	2,54,799.49	2.82	3	10,665.00	12,938.87	6- 32
15	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	21- 21
16	COMMERCE AND INDUSTRY	2	17,352.09	17,757.09	2.33	1	4,773.00	5,178.00	9- 9
Total		464	15,78,418.68	19,65,439.60	24.52	118	3,97,944.33	6,68,739.83	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-24

State-Wise Position of Central Sector Projects costing Rs. 1000 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	20	97,962.39	1,53,647.17	56.84	8	40,990.60	95,845.33	1 - 168
2	ARUNACHAL PRADESH	5	13,732.92	32,374.37	135.74	2	8,782.23	27,423.68	126 - 155
3	ASSAM	8	31,807.34	34,497.52	8.46	1	385.20	1,532.00	12 - 12
4	BIHAR	23	57,179.10	90,364.87	58.04	7	29,343.85	53,795.38	12 - 118
5	GUJARAT	21	69,363.23	74,844.09	7.90	3	14,247.62	19,884.04	8 - 69
6	HARYANA	15	21,618.98	24,638.36	13.97	1	1,108.00	2,967.50	100 - 100
7	HIMACHAL PRADESH	7	15,497.19	25,727.72	66.02	1	3,919.59	9,997.11	147 - 147
8	JAMMU AND KASHMIR	10	18,318.84	44,246.09	141.53	1	2,500.00	27,949.00	235 - 235
9	KARNATAKA	19	55,423.75	58,845.64	6.17	4	4,902.43	6,619.00	3 - 16
10	KERALA	9	30,871.86	34,724.00	12.48	4	12,006.19	14,204.10	18 - 44
11	MADHYA PRADESH	22	60,547.97	68,655.23	13.39	8	28,929.84	35,978.40	1 - 73
12	MAHARASHTRA	51	1,53,981.12	1,67,689.59	8.90	13	22,229.53	31,327.68	1 - 204
13	MANIPUR	1	4,454.17	12,524.00	181.17	1	4,454.17	12,524.00	132 - 132
14	MEGHALAYA	1	906.46	6,000.60	561.98	0	0.00	0.00	-
15	MIZORAM	1	2,393.47	5,021.45	109.80	1	2,393.47	5,021.45	96 - 96
16	NAGALAND	3	7,896.52	11,376.81	44.07	1	2,326.52	5,806.81	79 - 79
17	ODISHA	34	81,194.16	83,178.70	2.44	9	22,712.87	28,196.97	12 - 183
18	PUNJAB	3	3,627.54	4,826.70	33.06	1	1,388.34	2,587.50	6 - 6
19	RAJASTHAN	10	22,632.33	28,820.49	27.34	1	12,320.00	17,079.00	75 - 75
20	SIKKIM	1	1,339.48	4,084.69	204.95	0	0.00	0.00	-
21	TAMIL NADU	24	95,454.89	1,11,375.19	16.68	5	15,380.80	23,200.22	12 - 133
22	UTTAR PRADESH	43	1,12,731.46	1,18,937.71	5.51	5	23,116.58	27,149.38	3 - 40
23	WEST BENGAL	24	43,267.91	59,223.65	36.88	9	20,992.37	32,500.97	16 - 324
24	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	-
25	DELHI	10	81,740.38	83,303.70	1.91	3	10,256.21	11,898.73	6 - 17
26	CHHATISGARH	14	65,083.62	76,559.60	17.63	6	33,664.00	45,210.91	3 - 62
27	JHARKHAND	13	49,100.48	53,989.92	9.96	2	16,090.78	17,157.29	9 - 33
28	UTTARAKHAND	6	26,039.84	31,109.03	19.47	2	5,470.06	10,265.18	105 - 114
29	TELANGANA	5	18,567.06	20,644.30	11.19	0	0.00	0.00	-
30	MULTI STATE	60	3,29,598.14	4,38,366.10	33.00	19	58,033.08	1,02,618.20	9 - 252
Total		464	15,78,418.68	19,65,439.60	24.52	118	3,97,944.33	6,68,739.83	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-25

List of projects completed/dropped/Frozen during current month					Rs. 150		Crore and above	
(All Cost/ Expenditure in Rs. crore)								
			Original		Now anticipated			
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure	
	FERTILISERS							
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	11/2016	209.44	01/2020	188.89	
	PETROLEUM							
2	ASSAM RENEWAL PROJECT FOR GROUP A	03/2009	2,465.15	03/2013	2,378.86	12/2019	2,177.58	
3	POLYPROPYLENE PLANT AT PARADIP REFINERY	03/2014	3,150.00	09/2017	3,150.00	01/2020	2,573.02	
4	4TH PHASE DEVELOPMENT OF NBP FIELD Central Sector Projects	02/2017	968.61	11/2019	1,033.95	11/2019	968.11	
5	DEVELOPMENT OF BSE-11 BLOCK Central Sector Projects	02/2017	511.30	11/2019	511.30	11/2019	546.76	
6	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	06/2010	202.94	01/2014	345.92	11/2019	193.03	
7	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH	12/2016	300.00	04/2021	300.00	N.A.	1.09	
	POWER							
8	DHUKWAN SMALL HYDRO PROJECT	05/2011	195.42	02/2014	294.60	12/2019	322.23	
9	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	05/2005	1,779.29	11/2008	2,187.32	12/2019	2,294.33	
10	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA	04/2016	844.64	04/2019	844.64	11/2019	437.95	
11	SOUTHERN REGION STRENGTHENING SCHEME-XXI	09/2016	562.25	03/2019	562.25	12/2019	423.45	
12	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII	03/2017	337.75	06/2019	337.75	12/2019	176.71	
	WATER RESOURCES							
13	SEWERAGE WORKS IN SEWERAGE DISTRICT A OF ALLAHABAD	02/2014	288.94	09/2019	288.94	N.A.	246.99	

TABLE-26

List of projects added Rs. 150 Crore and above					(January 2020)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>COMMERCE AND INDUSTRY</u>					
1	DELHI MUMBAI INDUSTRIAL CORRIDOR	9/2011	12,579.09	9/2019	12,579.09	9/2020
2	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	4,773.00	12/2019	5,178.00	9/2020
	<u>PETROLEUM</u>					
3	LPG BP PROJECT CHITTOOR	7/2019	167.00	7/2022	167.00	7/2022
4	COMPRESSED BIO GAS PLANT AT GORAKHPUR	9/2019	164.69	7/2021	164.69	7/2021
5	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY	11/2019	5,251.00	5/2023	5,251.00	5/2023

TABLE-27

Milestones (Cumulative due & achieved)	Rs. 150	Crore and above
Total	5636	
Achieved up to month	2953	

TABLE-28

<u>List of projects reporting additional delayed</u> Rs. 150 Crore and above							(January 2020)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>ATOMIC ENERGY</u>						
1	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) NPCIL	12,320.00	17,079.00	12/2016	10/2022	03/2023	5
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 NPCIL	11,459.00	16,580.00	12/2015	03/2021	09/2021	6
	<u>COAL</u>						
3	MADHUBAND NLW WASHERY BCCL	289.45	289.45	05/2014	03/2020	05/2020	2
4	PATHERDIH NLW WASHERY BCCL	269.82	269.82	04/2014	01/2020	03/2020	2
	<u>FERTILISERS</u>						
5	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA NFL	218.83	218.83	11/2019	11/2019	05/2020	6
6	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL NFL	239.81	239.81	11/2019	11/2019	05/2020	6
	<u>STEEL</u>						
7	FORGED WHEEL PLANT RINL	1,682.85	1,682.85	09/2018	01/2020	02/2020	1
8	CENTRAL DISPATCH YARD RINL	320.66	320.66	08/2018	01/2020	02/2020	1
9	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT SAIL	1,154.18	1,154.18	12/2017	01/2020	03/2020	2
10	COKE OVEN BATTERY-5 RINL	2,858.00	2,500.00	12/2017	01/2020	03/2020	2
11	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL SAIL	262.87	262.87	06/2019	06/2020	11/2020	5
	<u>PETROLEUM</u>						
12	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY IOCL	598.00	598.00	02/2020	12/2020	01/2021	1
13	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) ONGC	861.79	1,683.06	05/2013	12/2019	02/2020	2

<u>List of projects reporting additional delayed</u> Rs. 150 Crore and above (January 2020)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
14	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY BPCL	4,588.29	5,245.96	08/2018	12/2019	02/2020	2
15	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND IOCL	236.00	236.00	06/2020	08/2020	10/2020	2
16	INTEGRATED DEVELOPMENT OF B-127 FIELDS ONGC	2,059.63	2,665.65	03/2015	12/2019	03/2020	3
17	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III ONGC	6,068.80	5,296.93	04/2019	12/2019	03/2020	3
18	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) ONGC	766.37	766.37	12/2019	12/2019	03/2020	3
19	BS-VI PROJECTS CPCL	1,858.00	1,858.00	12/2019	12/2019	04/2020	4
20	DAMAN DEVELOPMENT PROJECT ONGC	6,086.08	5,842.31	05/2019	10/2019	03/2020	5
21	RE-LIQUIFIED NATURAL GAS CPCL	421.00	421.00	08/2020	08/2020	02/2021	6
22	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY IOCL	909.00	909.00	01/2021	01/2021	08/2021	7
23	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY IOCL	206.63	206.63	02/2020	02/2020	12/2020	10
24	GRASS ROOT TERMINAL AT MALKAPUR IOCL	611.00	611.00	04/2022	04/2022	03/2023	11
	<u>POWER</u>						
25	SYSTEM STRENGTHENING XIII OF SR GRID PGCIL	487.49	639.46	06/2014	01/2020	02/2020	1
26	EASTERN REGION STRENGTHENING SCHEME-V PGCIL	1,364.52	1,891.41	04/2016	01/2020	02/2020	1
27	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH PGCIL	5,151.37	5,151.37	03/2018	02/2020	03/2020	1
28	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P PGCIL	14,733.37	14,733.37	11/2019	02/2020	03/2020	1
29	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI PGCIL Central Sector Projects	3,654.00	3,654.00	04/2019	12/2019	01/2020	1
30	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY PGCIL Central Sector Projects	186.17	186.17	07/2019	02/2020	03/2020	1

<u>List of projects reporting additional delayed</u> Rs. 150 Crore and above (January 2020)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
31	DARLIPALLI STPP STAGE-I (2X800 MW) NTPC	12,532.44	13,740.53	12/2018	06/2020	08/2020	2
32	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) PGCIL Central Sector Projects	445.89	445.89	02/2019	03/2020	05/2020	2
33	HVDC BIPOLE LINK BETWEEN WR AND SR - NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN PGCIL Central Sector Projects	1,931.39	1,931.39	02/2020	04/2020	06/2020	2
34	TELANGANA SUPER THERMAL POWER PROJECT PHASE I NTPC	10,598.98	10,598.98	11/2020	06/2021	09/2021	3
35	KAMENG HYDROELECTRIC PROJECT (NEEPCO) NEEPCO	2,496.90	7,927.34	12/2009	01/2020	06/2020	5
36	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL NTPC	1,885.13	1,885.13	12/2018	03/2020	08/2020	5
37	DURGAPUR PP-III (2X20 MW) - NSPCL NTPC	529.68	529.68	11/2018	03/2020	08/2020	5
	<u>HEALTH AND FAMILY WELFARE</u>						
38	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR CPWD	1,577.00	1,828.00	09/2025	09/2024	09/2025	12
	<u>RAILWAYS</u>						
39	AJMER-BANGURGRAM NWR	213.39	303.56	11/2019	10/2020	12/2020	2
40	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING SER	258.20	358.68	12/2018	06/2020	08/2020	2
41	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND SER	148.77	377.00	12/2016	01/2020	03/2020	2
42	DAUSA-GANGAPUR CITY(NL),NWR NWR	410.08	886.41	02/2019	03/2021	06/2021	3
43	BANGURGRAM-GURIYA PATCH DOUBLING NWR	246.08	348.55	12/2019	11/2020	02/2021	3
44	ANUPPUR-KATNI SECR	1,370.00	1,370.94	12/2021	11/2022	03/2023	4
45	ROURKELA JHARSUGUDA THIRD LINE 101 KM SER	969.83	1,312.96	03/2020	06/2020	03/2021	9
46	KOTTAVALSA - KORAPUT DOUBLING ECR	2,499.71	3,382.95	03/2022	03/2022	03/2024	24
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						

List of projects reporting additional delayed Rs. 150 Crore and above							(January 2020)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
47	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A NHAI	688.70	688.70	N.A.	01/2020	02/2020	1
48	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS MoRTH	233.04	233.04	03/2018	03/2020	04/2020	1
49	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM MoRTH	877.79	877.79	06/2019	06/2020	07/2020	1
50	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS MoRTH	162.56	162.56	03/2018	03/2020	05/2020	2
51	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID MoRTH	235.91	235.91	02/2018	03/2020	05/2020	2
52	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS MoRTH	184.62	184.62	02/2018	03/2020	05/2020	2
53	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 MoRTH	287.34	287.34	01/2019	01/2020	03/2020	2
54	REHABILITATION AND UPGRADATION OF HARPALPUR -SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE MoRTH	208.50	208.50	11/2019	01/2020	03/2020	2
55	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH MoRTH	240.30	240.30	01/2020	01/2020	03/2020	2
56	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 NHAI PPP (BOT)	1,535.00	1,535.00	05/2014	12/2019	03/2020	3
57	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II NHAI	795.76	677.72	N.A.	12/2019	03/2020	3
58	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION NHAI	479.00	479.00	N.A.	03/2020	06/2020	3
59	FOUR LANING OF YADGIRI - WARANGAL NHAI	1,423.96	897.03	11/2018	03/2020	06/2020	3
60	FOUR LANING OF AURANGABAD - YEDISHI NHAI PPP (BOT)	1,871.34	1,871.34	01/2018	12/2019	03/2020	3
61	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 NHAI	557.30	557.30	N.A.	03/2020	06/2020	3
62	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. MoRTH	205.05	205.05	03/2017	06/2020	09/2020	3
63	2L+PS OF THIKRI ANJAD SECTION OF NH-347B MoRTH	249.05	249.05	07/2018	03/2020	06/2020	3

List of projects reporting additional delayed Rs. 150 Crore and above (January 2020)							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
64	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS MoRTH	809.16	809.16	07/2018	06/2020	09/2020	3
65	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. MoRTH	392.33	428.55	03/2018	06/2020	09/2020	3
66	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A MoRTH	373.82	373.82	09/2019	05/2020	09/2020	4
67	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V MoRTH	429.43	429.43	11/2017	11/2019	03/2020	4
68	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA NHAI	229.37	229.37	11/2018	03/2020	08/2020	5
69	SIX-LANING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV NHAI	894.00	929.32	04/2020	11/2019	04/2020	5
70	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 MoRTH EPC	957.54	957.54	02/2020	02/2020	08/2020	6
71	FOUR LANING OF CHANDIGARH - KHARAR NHAI	447.29	746.43	12/2017	12/2019	06/2020	6
72	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) NHAI	1,388.34	2,587.50	09/2019	09/2019	03/2020	6
73	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS MoRTH	214.69	214.69	03/2018	06/2020	12/2020	6
74	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS MoRTH	254.17	254.17	02/2018	03/2020	09/2020	6
75	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 MoRTH	376.25	376.25	08/2017	08/2019	02/2020	6
76	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD MoRTH	319.28	319.28	08/2017	08/2019	03/2020	7
77	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 MoRTH EPC	628.45	628.45	01/2020	01/2020	09/2020	8
78	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS NHAI	364.56	392.00	N.A.	12/2019	08/2020	8
79	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER NHAI	648.32	511.94	03/2020	07/2019	03/2020	8


List of projects reporting additional delayed Rs. 150 Crore and above (January 2020)							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
80	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) NHAI	447.75	447.75	N.A.	11/2019	08/2020	9
81	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS MoRTH	247.25	247.25	03/2019	09/2019	06/2020	9
82	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 MoRTH	290.15	290.15	05/2017	05/2019	03/2020	10
83	4-LANNING OF THALSERRY -MAHE BYPASS NHAI Central Sector Projects	1,124.11	1,232.76	09/2017	06/2020	05/2021	11
84	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE NHAI	290.73	315.00	N.A.	03/2019	03/2020	12
85	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 MoRTH	1,069.59	1,069.59	10/2019	10/2019	12/2020	14
86	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 MoRTH	263.45	263.45	09/2017	09/2019	12/2020	15
87	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN NHAI	754.54	756.27	03/2020	04/2020	08/2021	16
88	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 MoRTH	444.84	444.84	09/2016	09/2018	03/2020	18
89	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT MoRTH	348.95	348.95	08/2016	08/2018	03/2020	19
90	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD MoRTH	350.61	350.61	01/2017	07/2018	04/2020	21
91	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O MoRTH	995.09	995.09	05/2016	05/2018	07/2020	26
92	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES MoRTH EPC	271.45	271.45	10/2015	10/2017	01/2020	27
93	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 MoRTH	333.21	355.89	12/2015	12/2016	01/2020	37
	<u>TELECOMMUNICATIONS</u>						
94	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT BSNL Central Sector Projects	231.80	240.10	10/2018	01/2020	02/2020	1

<u>List of projects reporting additional delayed</u> Rs. 150 Crore and above (January 2020)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
	<u>URBAN DEVELOPMENT</u>						
95	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI CPWD	197.33	197.33	04/2019	11/2020	12/2020	1
96	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB CPWD	430.00	387.83	05/2020	01/2021	02/2021	1
97	REDEVELOPMENT OF EAST KIDWAI NAGAR NBCC	4,264.00	4,720.73	11/2019	03/2020	05/2020	2
98	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB CPWD	388.00	490.00	05/2017	01/2020	03/2020	2
99	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB CPWD	294.00	350.69	04/2019	03/2020	05/2020	2
100	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN CPWD	549.31	559.47	07/2019	04/2020	08/2020	4
	<u>WATER RESOURCES</u>						
101	POLAVARAM IRRIGATION PROJECT PPA National Project	10,151.04	55,548.87	03/2020	06/2021	12/2021	6


TABLE-29

Sector wise analysis of projects Rs. 150 Crore and above					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	67,120.00	693,05.00	80,348.00	50,215.38
CIVIL AVIATION	13	8,607.51	86,07.51	8,734.44	1,357.47
COAL	107	1,04,637.11	1,053,68.36	1,08,558.02	38,613.72
FERTILISERS	4	1,101.28	11,01.28	1,101.28	701.67
MINES	5	7,078.62	70,75.17	7,075.17	673.31
STEEL	9	26,228.23	338,43.23	33,485.23	24,413.37
PETROLEUM	148	2,69,889.88	2,838,51.38	2,84,938.40	1,01,562.39
POWER	64	2,73,781.33	3,063,00.66	3,44,106.51	2,22,894.97
HEAVY INDUSTRY	1	1,554.00	15,54.00	1,554.00	716.25
HEALTH AND FAMILY WELFARE	23	12,454.56	125,74.56	12,796.11	5,325.26
RAILWAYS	312	4,59,394.75	5,829,61.69	6,71,692.95	2,06,153.91
ROAD TRANSPORT AND HIGHWAYS	867	5,13,537.42	5,362,39.81	5,28,085.90	3,00,798.25
SHIPPING AND PORTS	1	4,200.00	53,69.18	5,369.18	1,540.69
TELECOMMUNICATIONS	4	16,095.23	161,03.53	27,333.53	12,886.86
URBAN DEVELOPMENT	74	2,63,824.96	2,654,86.30	2,71,185.14	92,748.02
WATER RESOURCES	50	26,999.51	724,57.43	72,397.34	34,804.54
COMMERCE AND INDUSTRY	2	17,352.09	173,52.09	17,757.09	2,088.58
HUMAN RESOURCE DEVELOPMENT	4	1,356.22	13,56.22	1,498.16	110.00
Grand total	1692	20,75,212.70	23,26,907.40	24,78,016.45	10,97,604.64

Graphical Presentation of All Projects w.r.t. Original Schedule

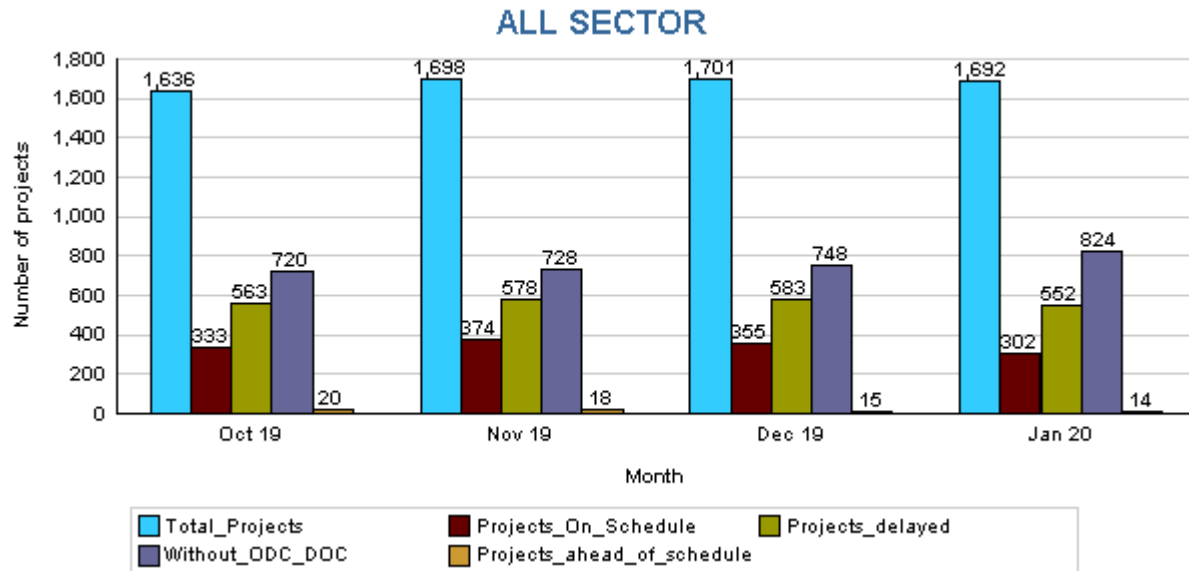


Break-up of 552 Delayed projects in January 2020

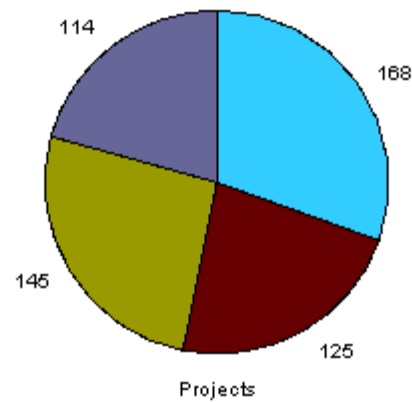


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

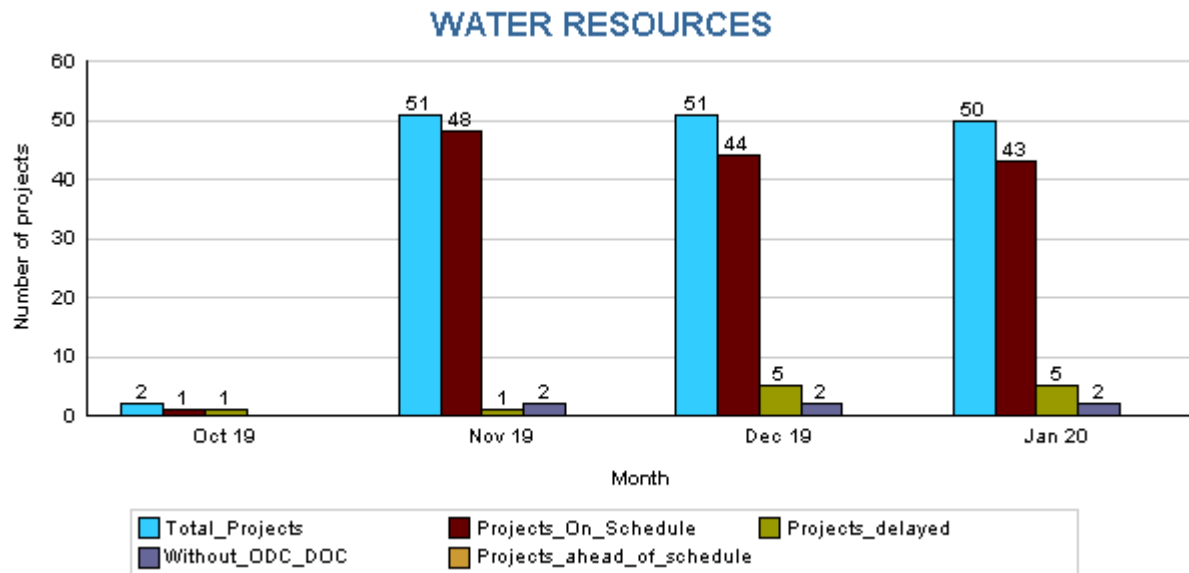


Break-up of 5 Delayed projects in January 2020

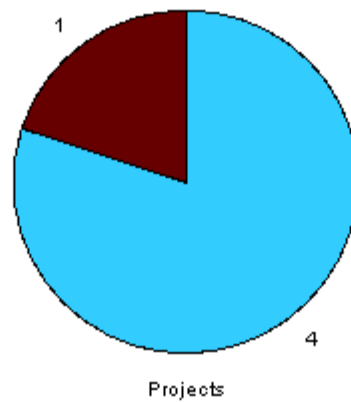


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

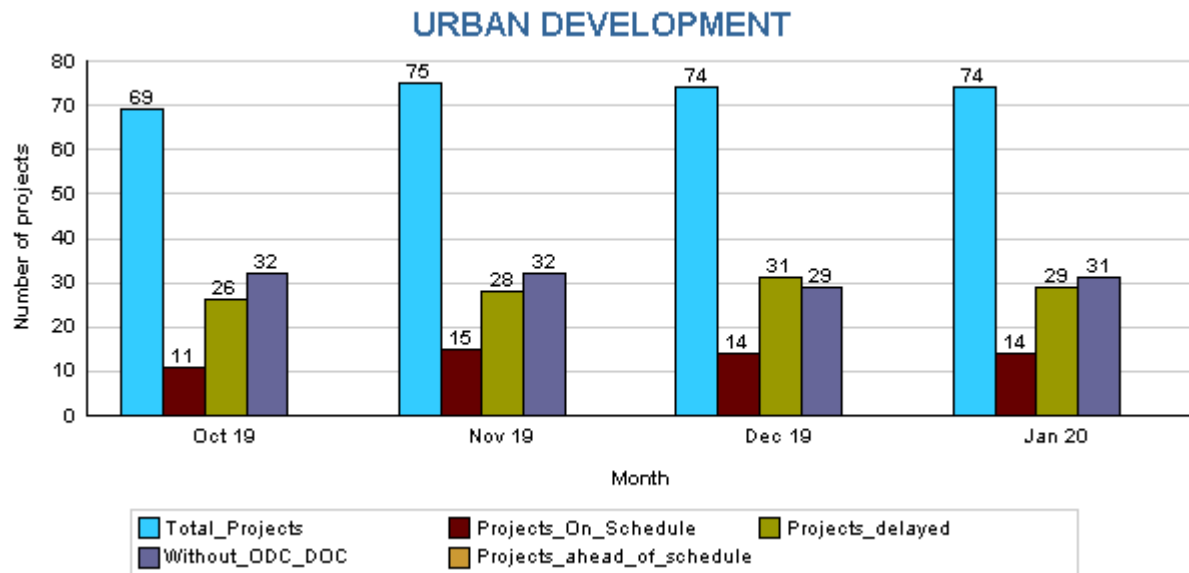


Break-up of 29 Delayed projects in January 2020

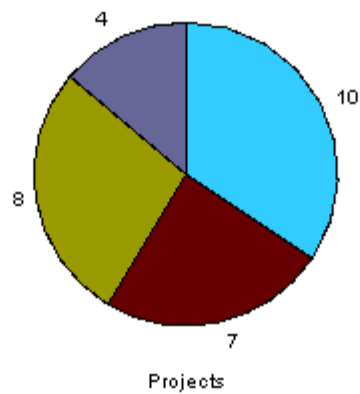


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

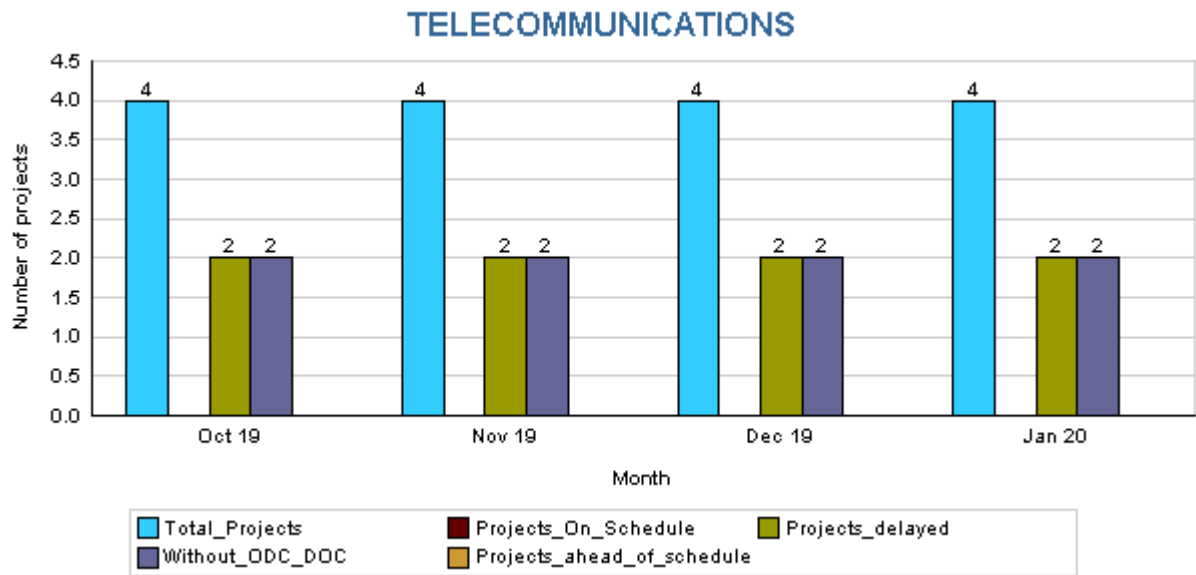


Break-up of 2 Delayed projects in January 2020

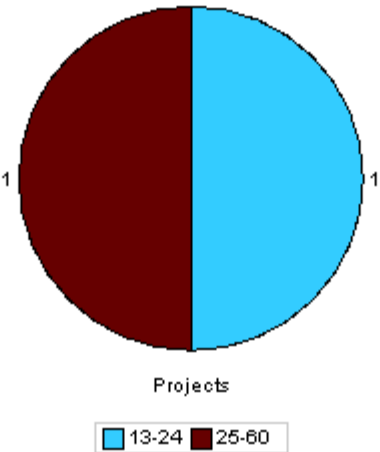


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

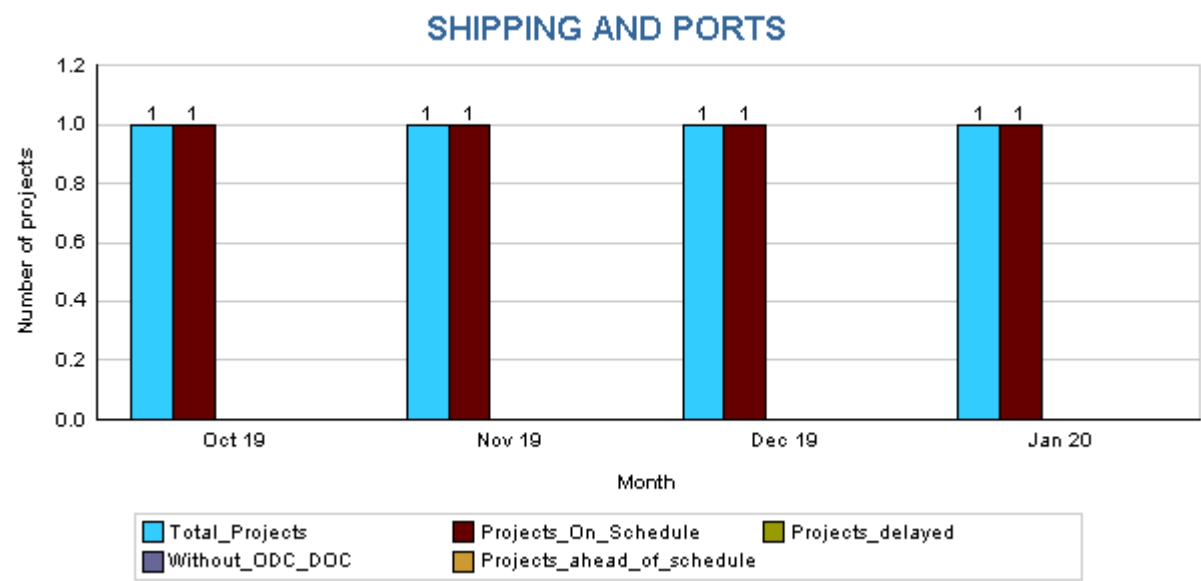


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

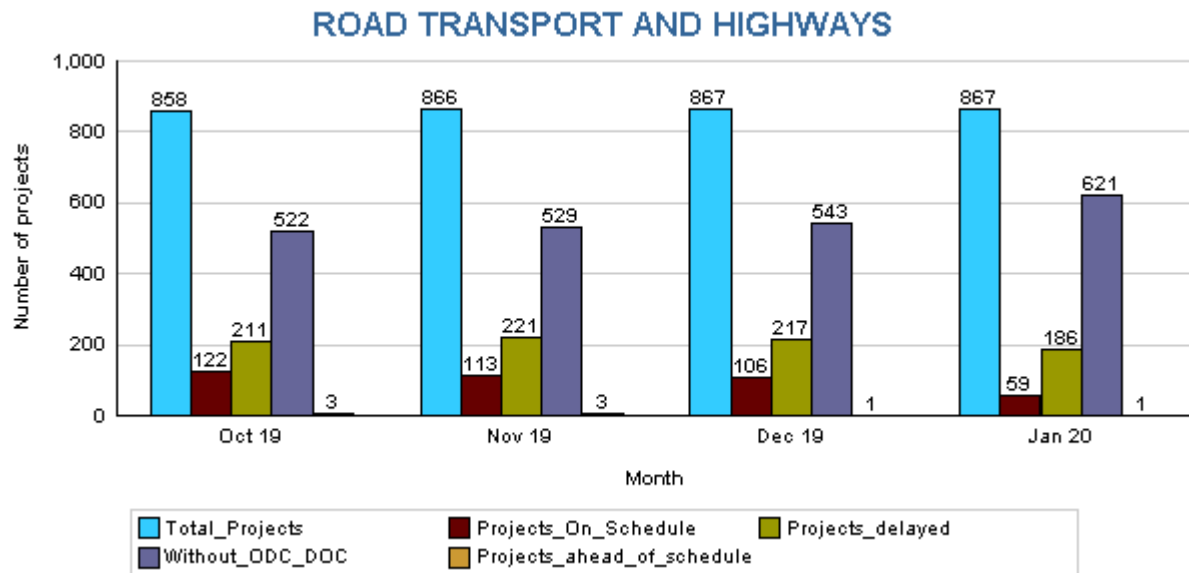


Break-up of 186 Delayed projects in January 2020

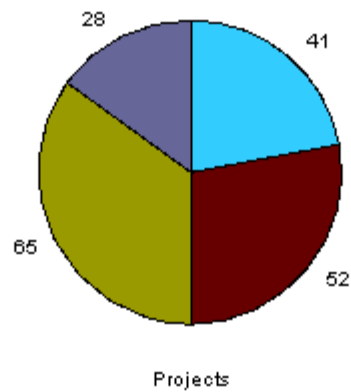


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

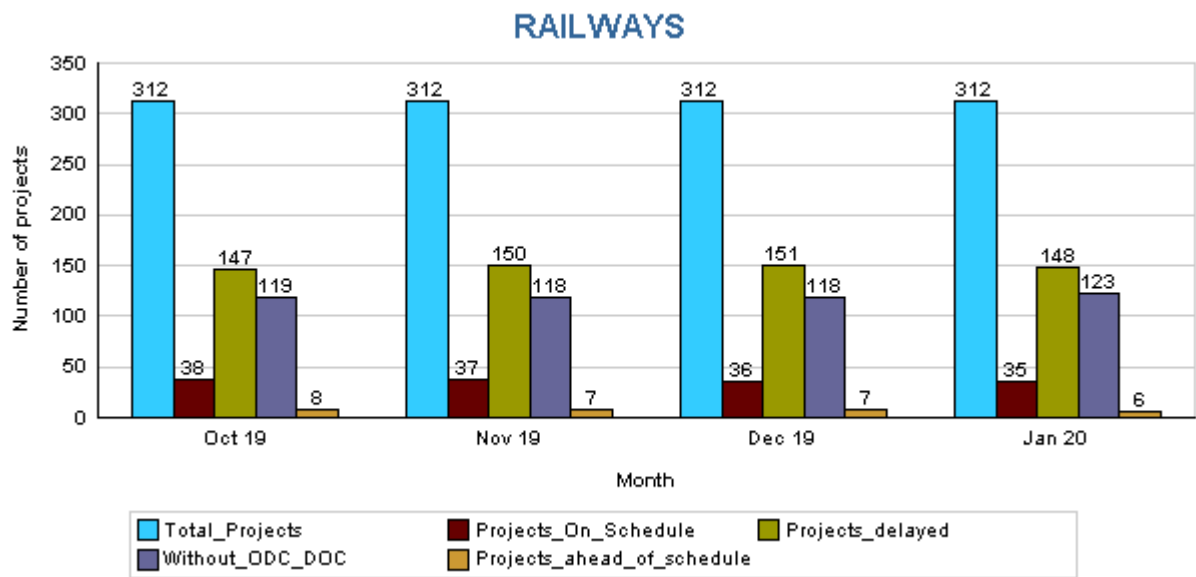

Break-up of 148 Delayed projects in January 2020

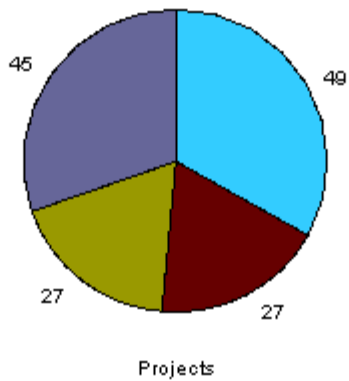

Delay in Months


1-12

13-24


25-60

60 and Above

Graphical Presentation of All Projects w.r.t. Original Schedule

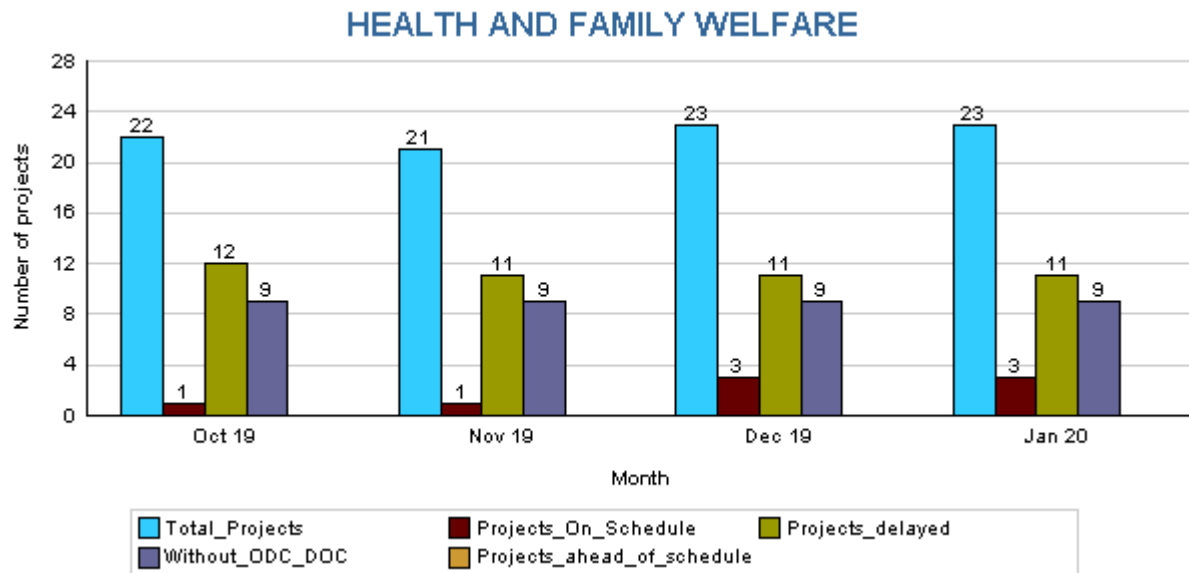


Break-up of 11 Delayed projects in January 2020

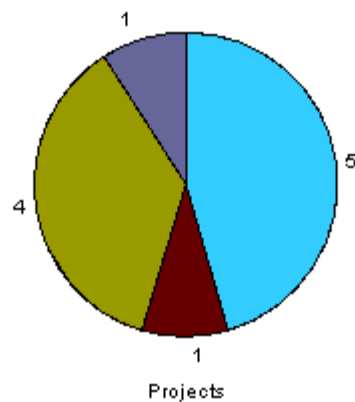


Delay in Months

1-12	13-24	25-60	60 and Above

Graphical Presentation of All Projects w.r.t. Original Schedule

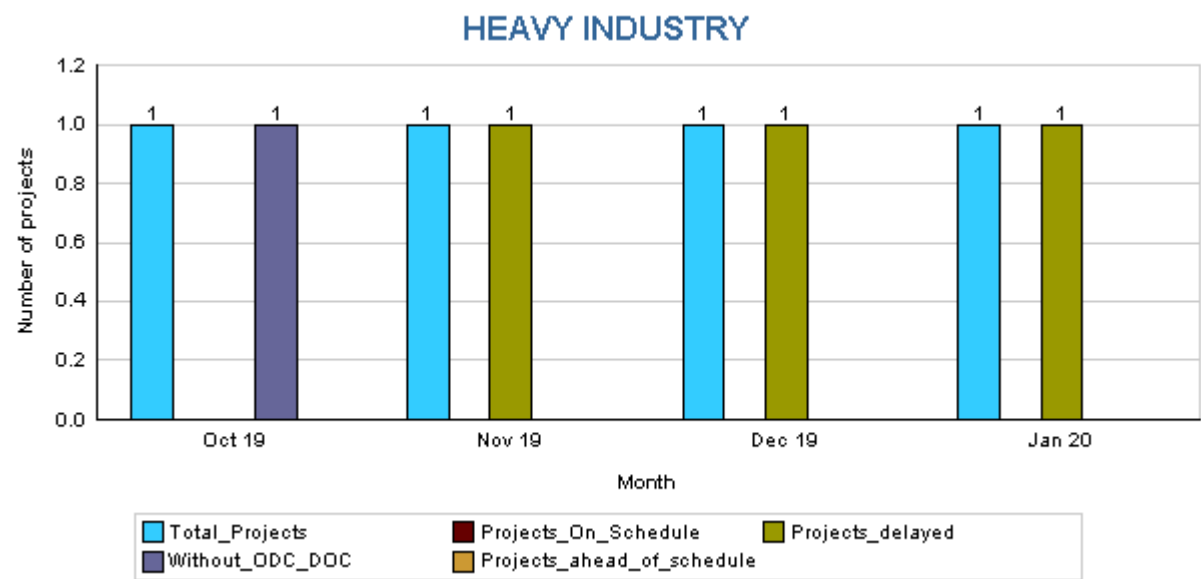


Break-up of 1 Delayed projects in January 2020

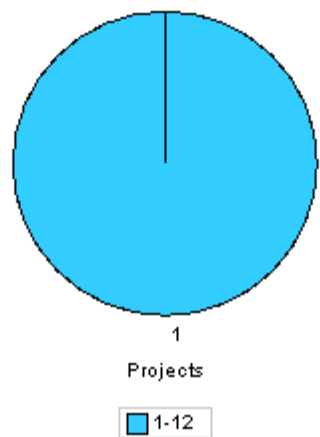


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

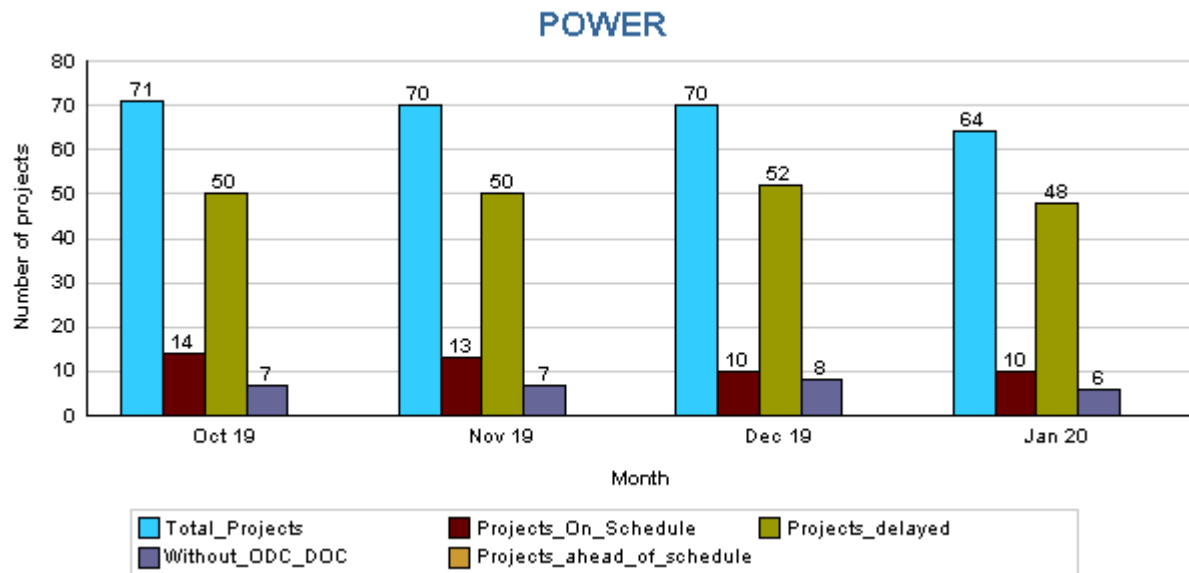


Break-up of 48 Delayed projects in January 2020

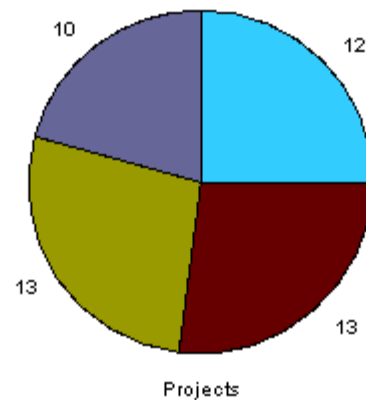


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

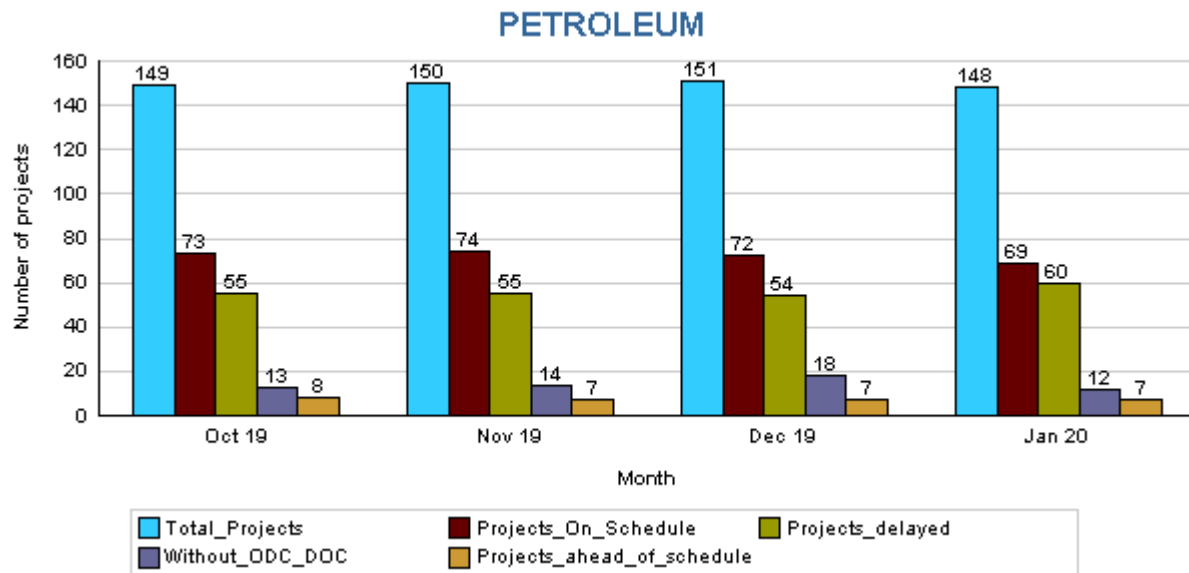


Break-up of 60 Delayed projects in January 2020

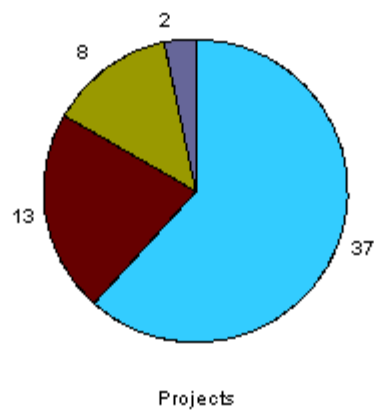


Delay in Months




Graphical Presentation of All Projects w.r.t. Original Schedule

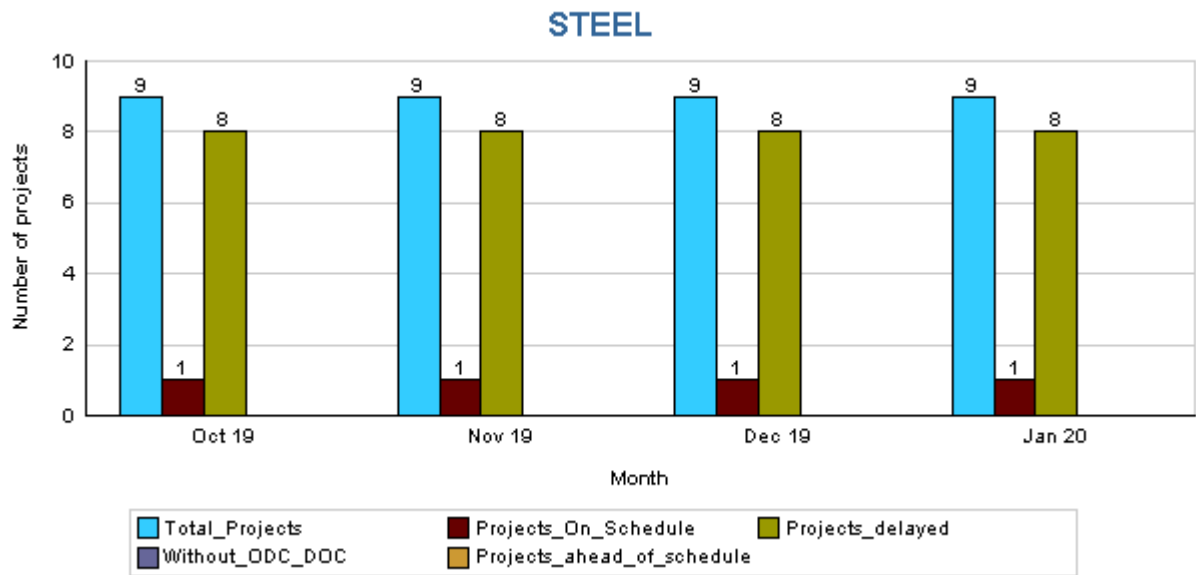


Break-up of 8 Delayed projects in January 2020

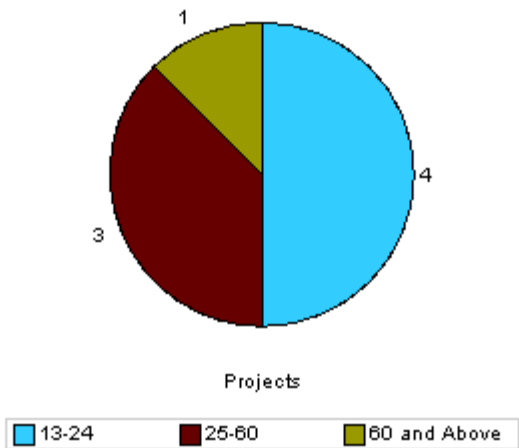


Graphical Presentation of All Projects w.r.t. Original Schedule

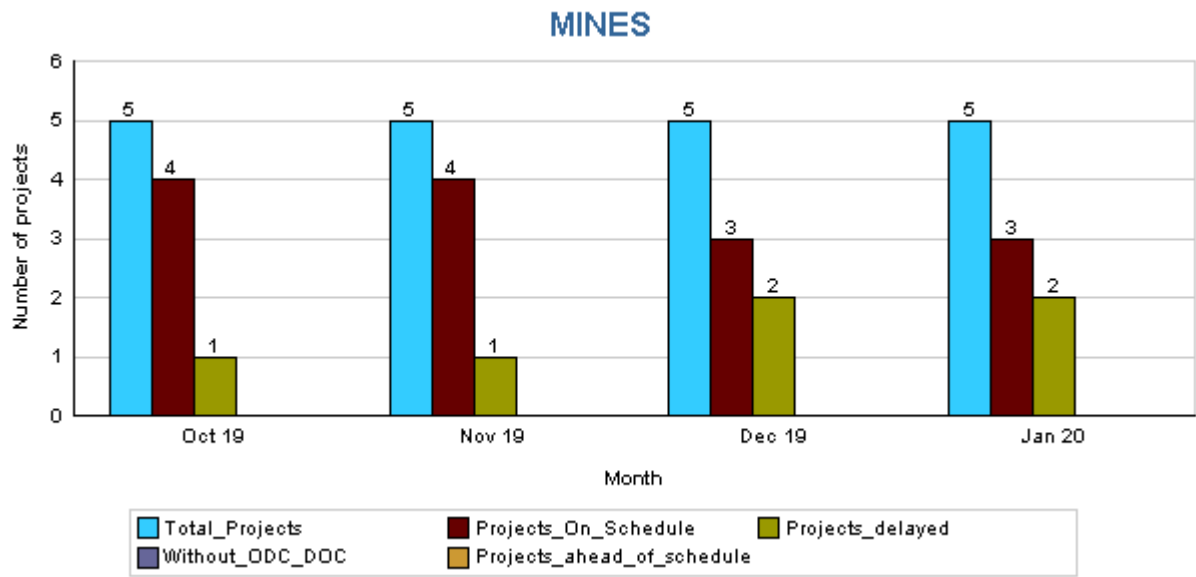


Break-up of 2 Delayed projects in January 2020




Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

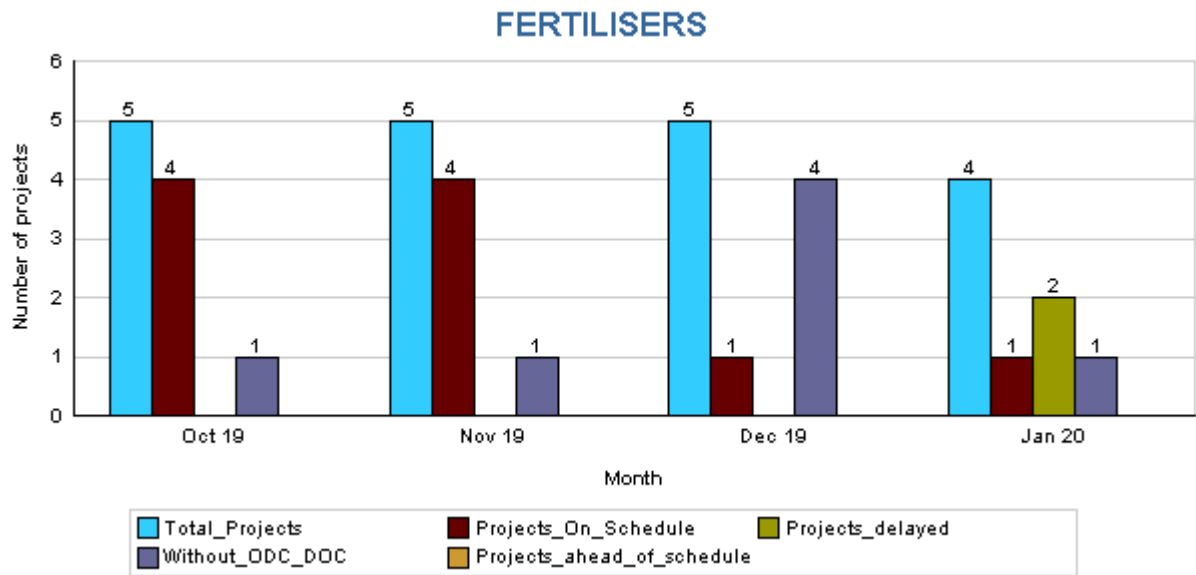


Break-up of 2 Delayed projects in January 2020




Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

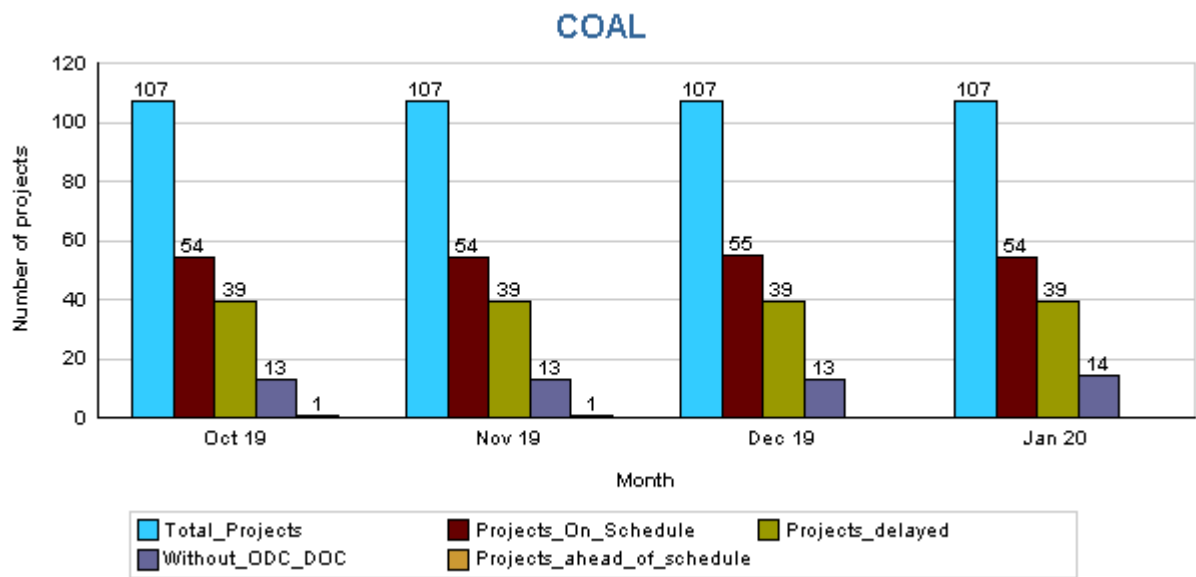


Break-up of 39 Delayed projects in January 2020

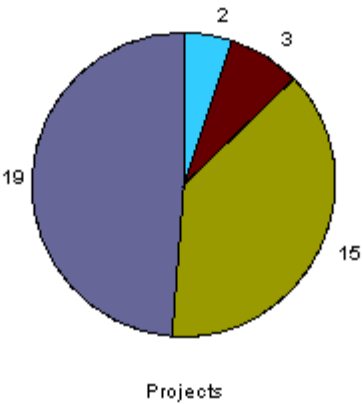


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

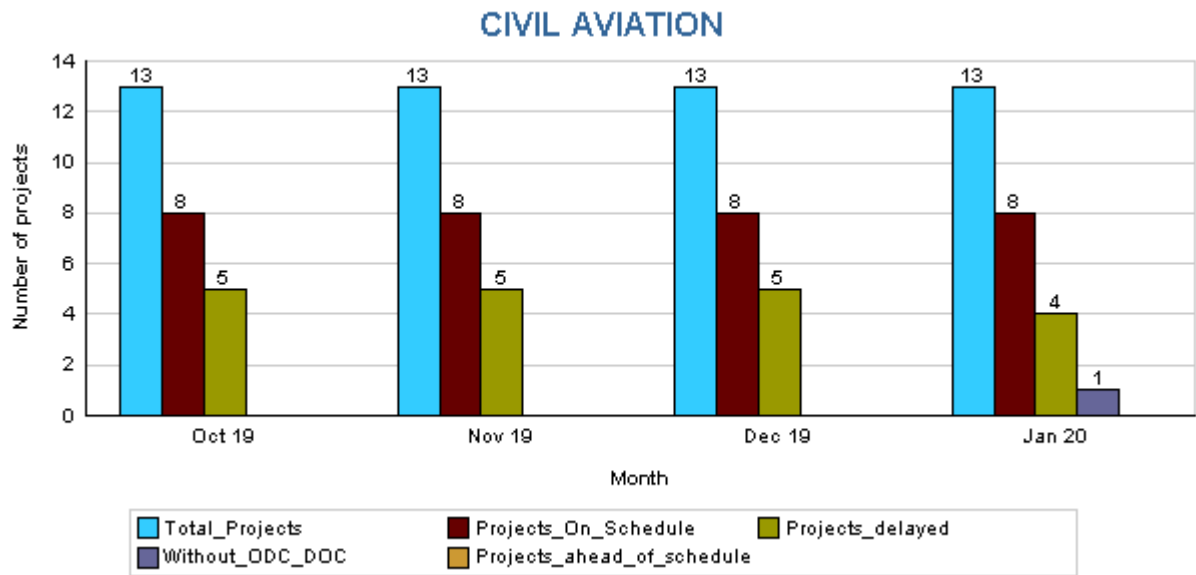


Break-up of 4 Delayed projects in January 2020

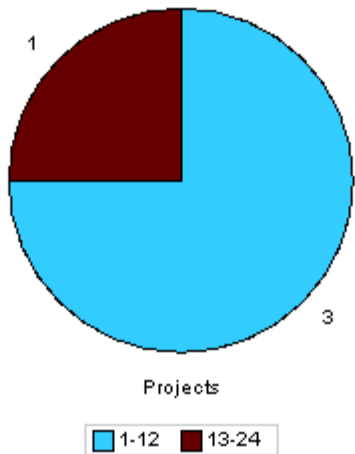


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

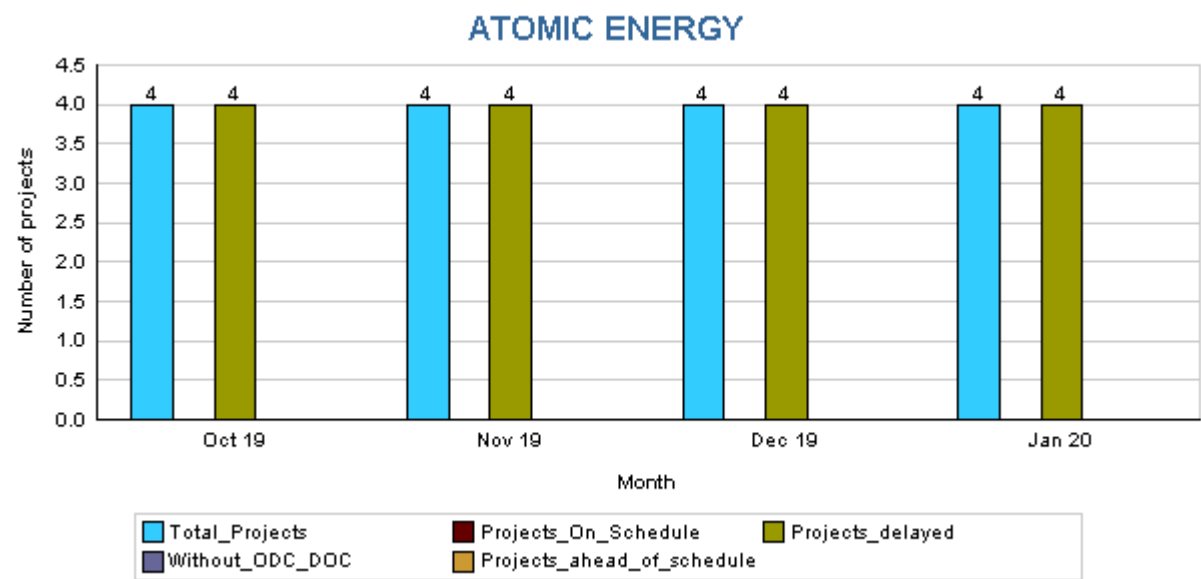

Break-up of 4 Delayed projects in January 2020

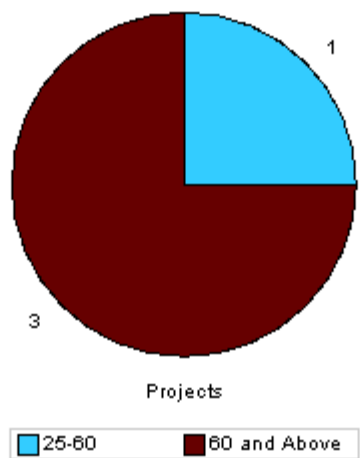

Delay in Months

TABLE-30

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT ,	10/2009	11,459.00 -	16,580.00	14,629.00	12/2015 -	09/2021	69(O) -	54/70
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN ,	10/2009	12,320.00 -	17,079.00	11,737.00	12/2016 -	03/2023	75(O) -	41/68
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI 500 MWE) - [020100044]BHAVNI,TAMIL NADU ,	09/2003	3,492.00 5,677.00	6,840.00	5,862.38	09/2010 09/2016	10/2021	133(O) 0	83/87
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL,TAMIL NADU , Central Sector Projects	03/2013	39,849.00 -	39,849.00	17,987.00	11/2020 -	11/2023	36(O) -	26/76
	Total		67,120.00 -	80,348.00	50,215.38				204/301
	<u>CIVIL AVIATION</u>								
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT PORTBLAIR - [N04000073]AAI,A & N ISLANDS ,	10/2013	314.61 -	441.33	85.79	09/2018 -	06/2020	21(O) -	0/0
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]AAI,ASSAM ,	12/2016	859.86 -	860.00	232.44	03/2021 -	03/2021	0(O) -	0/0
7	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES PHASE I AND II - [N04000082]AAI,BIHAR ,	05/2018	539.20 -	539.20	25.64	10/2022 -	10/2022	0(O) -	0/0
8	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA BCAS AAIB AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076]AAI,DELHI ,	11/2016	233.38 -	233.38	84.73	04/2020 -	12/2020	8(O) -	0/0
9	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]AAI,JAMMU AND KASHMIR ,	07/2018	323.19 -	323.19	10.14	09/2021 -	09/2021	0(O) -	0/0
10	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING RECONSTRUCTION OF OLD TERMINAL BUILDING MODIFICAT - [N04000079]AAI,MAHARASHTRA ,	03/2017	358.89 -	358.89	29.73	04/2021 -	04/2021	0(O) -	0/0
11	MODERNIZATION OF CHENNAI AIRPORT PHASE II CHENNAI - [N04000074]AAI,TAMIL NADU ,	06/2018	2,467.00 -	2,467.00	213.17	02/2022 -	08/2022	6(O) -	0/0
12	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]AAI,TAMIL NADU ,	08/2018	951.28 -	951.28	71.55	10/2021 -	10/2021	0(O) -	0/0
13	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI,TRIPURA ,	09/2015	338.93 -	339.00	213.50	06/2019 -	-	-	0/0
14	CCS INTERNATIONAL AIRPORT LUCKNOW - [N04000077]AAI,UTTAR PRADESH ,	06/2018	1,383.00 -	1,383.00	210.62	09/2021 -	09/2021	0(O) -	0/0
15	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT DEHRADUN - [N04000085]AAI,UTTARAKHAND ,	07/2018	353.27 -	353.27	114.29	09/2020 -	09/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
16	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA - [N04000080]AAI, WEST BENGAL ,	01/2016	219.91 -	219.91	65.45	03/2020 -	12/2020	9(O) -	0/0
17	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT KOLKATA - [N04000081]AAI, WEST BENGAL ,	01/2019	264.99 -	264.99	.42	11/2021 -	11/2021	0(O) -	0/0
	Total		8,607.51 -	8,734.44	1,357.47				0/0
	<u>COAL</u>								
18	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL, CHHATISGARH ,	06/2010	11,816.40 -	11,816.40	2,920.18	03/2023 03/2016	03/2023	0(O) 0	14/19
19	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL, CHHATISGARH ,	08/2013	7,612.33 -	7,612.33	2,358.32	03/2023 -	03/2023	0(O) -	7/21
20	PELMA OCP(15.00MTY) - [N06000045]SECL, CHHATISGARH ,	11/2014	1,624.59 -	1,624.59	6.58	03/2023 -	03/2023	0(O) -	1/12
21	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL, CHHATISGARH ,	09/2008	152.43 459.49	459.49	195.34	03/2015 03/2020	03/2020	60(O) 0	6/10
22	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH ,	07/2008	178.44 -	178.44	2.92	03/2014 -	03/2020	72(O) -	2/8
23	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH ,	12/2009	321.50 -	321.50	197.36	03/2014 -	03/2021	84(O) -	0/5
24	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL, CHHATISGARH ,	04/2012	258.56 -	258.56	182.04	03/2016 -	03/2020	48(O) -	4/7
25	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL, CHHATISGARH ,	12/2013	610.63 -	610.63	110.31	03/2022 -	03/2022	0(O) -	2/10
26	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL, CHHATISGARH ,	05/2014	164.49 -	164.49	81.59	03/2020 -	03/2020	0(O) -	5/9
27	AMERA OC RCE - [N06000123]SECL, CHHATISGARH ,	02/2015	335.97 -	335.97	51.21	03/2018 -	03/2020	24(O) -	1/7
28	AMGAON OPENCAST PROJECT RCE - [N06000135]SECL, CHHATISGARH ,	07/2015	316.10 -	316.10	88.82	03/2020 -	03/2020	0(O) -	1/6
29	DURGAPUR OPENCAST PROJECT - [N06000136]SECL, CHHATISGARH ,	02/2015	916.24 -	916.24	4.94	03/2023 -	03/2023	0(O) -	1/11
30	MADANNAGAR OPENCAST PROJECT - [N06000140]SECL, CHHATISGARH ,	10/2015	1,875.32 -	1,875.32	.00	03/2024 -	03/2024	0(O) -	1/5
31	VIJAY WEST OPENCAST PROJECT - [N06000158]SECL, CHHATISGARH ,	05/2017	976.95 -	976.95	75.96	03/2026 -	03/2026	0(O) -	0/1
32	MAHAMAYA OPENCAST PROJECT - [N06000164]SECL, CHHATISGARH ,	05/2018	410.26 -	410.26	9.53	03/2026 -	03/2026	0(O) -	0/1
33	JHIRIA WEST OPENCAST PROJECT - [N06000166]SECL, CHHATISGARH ,	11/2018	389.97 -	389.97	.00	03/2026 -	03/2026	0(O) -	1/1
34	MAGADH OC 20 MTY (CCL) - [N06000015]CCL, JHARKHAND ,	08/2008	706.40 -	706.40	501.09	07/2012 -	03/2022	116(O) -	6/6
35	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL, JHARKHAND ,	08/2007	163.51 -	163.51	107.16	03/2011 -	03/2021	120(O) -	6/6
36	TAPIN OCP (2.5 MTY) - [N06000086]CCL, JHARKHAND ,	08/2008	264.68 -	264.68	181.17	03/2012 -	03/2021	108(O) -	6/6
37	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL, JHARKHAND ,	12/2009	510.85 -	510.85	399.09	03/2016 -	03/2021	60(O) -	5/6
38	KARMA OCP (1.0MTY) - [N06000088]CCL, JHARKHAND ,	06/2009	162.46 -	162.46	90.75	03/2014 -	03/2021	84(O) -	6/6

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
39	MURADIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND ,	02/2011	339.88 -	339.88	12.08	04/2014 -	-	-	4/7
40	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND ,	08/2011	1,230.27 -	1,230.27	414.42	04/2015 04/2022	04/2022	84(O) 0	2/6
41	AMRAPALI OC(12MTY) - [N06000103]CCL,JHARKHAND ,	02/2012	858.11 -	858.11	190.41	03/2020 -	03/2020	0(O) -	6/7
42	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND ,	02/2014	555.52 -	555.52	5.38	03/2021 -	03/2021	0(O) -	0/2
43	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND ,	08/2011	988.35 -	988.35	45.26	04/2017 -	-	-	1/3
44	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND ,	08/2010	289.45 -	289.45	263.37	05/2014 03/2020	05/2020	72(O) 2	0/8
45	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND ,	10/2012	269.82 -	269.82	181.30	04/2014 -	03/2020	71(O) -	0/10
46	HURA - C OC (3 MTY) - [N06000143]ECL,JHARKHAND ,	10/2015	359.69 -	359.69	112.11	03/2022 -	03/2022	0(O) -	4/22
47	CHITRA EAST (RCE) OCP - [N06000169]ECL,JHARKHAND ,	08/2018	513.98 -	513.98	93.85	03/2024 -	03/2024	0(O) -	0/16
48	NORTH URIMARI EXPANSION OCP - [N06000182]CCL,JHARKHAND ,	03/2019	1,553.06 -	1,553.06	204.04	03/2023 -	03/2023	0(O) -	0/1
49	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH ,	02/2015	481.60 -	481.60	.00	03/2023 -	03/2023	0(O) -	2/9
50	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH ,	12/2014	357.80 -	357.80	104.77	03/2021 -	03/2021	0(O) -	3/10
51	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH ,	12/2014	371.04 -	371.04	48.13	03/2021 -	03/2021	0(O) -	3/8
52	BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH ,	07/2015	231.92 -	231.92	.00	03/2022 -	03/2022	0(O) -	1/8
53	MALACHUA OPENCAST PROJECT - [N06000139]SECL,MADHYA PRADESH ,	10/2015	488.33 -	488.33	27.33	03/2023 -	03/2023	0(O) -	0/4
54	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH ,	03/2016	869.44 -	869.44	117.99	03/2021 -	03/2021	0(O) -	2/5
55	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL,MADHYA PRADESH ,	07/2016	409.87 -	409.87	19.96	03/2022 -	03/2022	0(O) -	0/0
56	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL,MADHYA PRADESH , Central Sector Projects	05/2017	1,783.09 -	1,783.09	292.75	03/2021 -	03/2021	0(O) -	2/9
57	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]NCL,MADHYA PRADESH ,	11/2017	1,255.17 -	1,255.17	123.08	03/2022 -	03/2022	0(O) -	1/9
58	SEMARIA OPENCAST PROJECT - [N06000176]NCL,MADHYA PRADESH ,	05/2019	396.58 -	396.58	.00	03/2026 -	03/2026	0(O) -	1/5
59	VISHNUPURI UG TO OC MINE - [N06000178]WCL,MADHYA PRADESH ,	07/2018	195.57 -	195.57	2.94	03/2025 -	03/2025	0(O) -	0/7
60	GANDHIGRAM UG MINE - [N06000183]WCL,MADHYA PRADESH ,	08/2019	414.16 -	414.16	.50	03/2026 -	03/2026	0(O) -	0/7
61	BLOCK-B EXPANSION OPENCAST PROJECT - [N06000184]NCL,MADHYA PRADESH ,	07/2019	998.71 -	998.71	.00	03/2023 -	03/2023	0(O) -	0/7
62	PENGANGA OCP(REVISED) - [N06000066]WCL,MAHARASHTRA ,	09/2014	441.82 -	441.82	218.63	03/2020 -	03/2020	0(O) -	8/11
63	DINESH OCP - [N06000118]WCL,MAHARASHTRA ,	11/2014	611.16 -	611.16	415.50	03/2020 -	03/2020	0(O) -	3/8

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
64	BHANEAGON OC - [N06000121]WCL,MAHARASHTRA ,	02/2015	187.94 -	409.68	129.61	03/2023 -	03/2023	0(O) -	7/11
65	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA ,	05/2015	295.56 -	295.56	121.46	03/2019 -	-	-	10/13
66	SINGHORI OC MINE - [N06000130]WCL,MAHARASHTRA ,	06/2015	205.49 -	205.49	120.69	03/2020 -	03/2020	0(O) -	6/10
67	AMALGAMATED PAUNI-II III OC MINE - [N06000131]WCL,MAHARASHTRA ,	06/2015	483.69 -	483.69	225.02	03/2021 -	03/2021	0(O) -	3/6
68	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]WCL,MAHARASHTRA ,	08/2015	727.28 -	727.28	263.81	03/2025 -	03/2025	0(O) -	6/13
69	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA ,	08/2015	288.90 -	333.43	38.82	03/2023 -	03/2024	12(O) -	3/10
70	KAMPTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA ,	11/2015	277.65 -	313.34	118.18	03/2021 -	03/2024	36(O) -	3/6
71	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]WCL,MAHARASHTRA ,	11/2015	498.42 -	498.42	202.03	03/2020 -	03/2020	0(O) -	2/6
72	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL,MAHARASHTRA ,	02/2016	198.68 -	198.68	190.04	03/2019 -	-	-	3/9
73	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA ,	02/2016	304.52 -	304.52	155.34	03/2019 -	-	-	4/8
74	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL,MAHARASHTRA ,	03/2017	362.73 -	362.73	322.62	03/2020 -	03/2020	0(O) -	0/0
75	SAONER I UG TO OC PHASE I - [N06000177]WCL,MAHARASHTRA ,	11/2016	162.10 -	162.10	51.16	03/2022 -	03/2022	0(O) -	0/6
76	UKNI DEEP OC - [N06000179]WCL,MAHARASHTRA ,	11/2018	318.14 -	318.14	148.14	03/2021 -	03/2021	0(O) -	0/4
77	BELLORA-NAIGAON DEEP OC - [N06000180]WCL,MAHARASHTRA ,	11/2018	252.71 -	252.71	58.07	03/2021 -	03/2021	0(O) -	0/3
78	GAURI DEEP OC - [N06000181]WCL,MAHARASHTRA ,	10/2016	164.96 -	164.96	95.86	03/2019 -	-	-	1/3
79	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]WCL,MULTI STATE ,	08/2016	319.76 -	319.76	190.69	03/2022 -	03/2022	0(O) -	0/3
80	DHANKASA UG (1.00 MTY) - [N06000155]WCL,MULTI STATE ,	09/2016	458.07 -	458.07	22.46	03/2022 -	03/2022	0(O) -	1/12
81	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL,MULTI STATE ,	02/2017	328.00 -	328.00	186.61	03/2021 -	03/2021	0(O) -	3/6
82	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA ,	01/2005	302.96 -	302.96	270.32	03/2010 -	03/2020	120(O) -	10/10
83	BHUBANESWARI OCP MCL (20.0 MTY) - [N06000034]MCL,ODISHA ,	12/2007	490.10 -	490.10	524.33	03/2017 -	03/2021	48(O) -	11/12
84	KANIHA OCP MCL (10.0 MTY) - [N06000035]MCL,ODISHA ,	12/2007	457.77 -	457.77	568.14	03/2013 -	03/2022	108(O) -	8/9
85	BALRAM OCP EXTENSION MCL 8.00 MTY - [N06000044]MCL,ODISHA ,	12/2007	172.08 -	172.08	377.07	03/2010 -	03/2022	144(O) -	3/4
86	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA ,	08/2008	207.28 -	207.28	306.94	03/2012 -	03/2021	108(O) -	5/7
87	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA ,	11/2008	479.53 -	479.53	445.05	03/2013 -	03/2022	108(O) -	6/9
88	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA ,	05/2014	479.15 -	479.15	214.07	03/2019 -	03/2024	60(O) -	2/9
89	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA ,	05/2014	3,756.36 -	3,756.36	1,213.54	03/2026 -	03/2026	0(O) -	7/15

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
90	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA ,	05/2014	337.66 -	337.66	215.55	03/2019 -	03/2021	24(O) -	5/6
91	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA ,	06/2014	289.03 -	289.03	.00	03/2018 -	03/2021	36(O) -	5/6
92	GARJANBAHAL OCP - [N06000117]MCL,ODISHA ,	11/2014	1,375.38 -	1,375.38	445.23	03/2021 -	03/2021	0(O) -	7/9
93	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]MCL,ODISHA ,	05/2018	2,434.75 -	2,434.75	140.36	03/2027 -	03/2027	0(O) -	2/12
94	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]MCL,ODISHA ,	11/2018	2,838.87 -	2,838.87	1,169.40	03/2029 -	03/2029	0(O) -	0/9
95	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN , Central Sector Projects	03/2015	522.45 -	522.45	9.88	09/2019 -	-	-	0/0
96	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN , Central Sector Projects	03/2015	513.63 -	513.63	175.30	12/2019 -	-	-	0/0
97	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU ,	06/2011	5,907.11 7,080.41	7,080.41	6,954.15	12/2015 -	03/2020	51(O) -	32/35
98	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU ,	04/2013	1,458.17 709.06	709.06	462.63	06/2015 -	-	-	5/7
99	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA ,	10/2006	249.03 -	448.86	326.69	03/2012 -	03/2024	144(O) -	36/42
100	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA ,	12/2008	453.63 -	453.63	121.91	12/2012 -	-	-	11/44
101	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA ,	12/2009	418.97 -	489.62	416.88	03/2012 -	03/2023	132(O) -	1/2
102	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA ,	03/2010	209.78 -	209.78	137.06	03/2015 -	03/2020	60(O) -	30/31
103	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA ,	03/2010	181.19 -	181.19	170.60	03/2012 -	-	-	6/6
104	KISTARAM OCP - [N06000089]SCCL,TELANGANA ,	11/2010	242.29 -	164.04	120.31	03/2015 -	03/2021	72(O) -	3/5
105	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA ,	07/2011	162.76 -	349.28	12.27	03/2015 -	03/2021	72(O) -	5/29
106	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA ,	07/2011	447.06 -	473.22	18.60	03/2015 -	03/2021	72(O) -	8/13
107	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA ,	06/2012	365.01 -	365.01	171.06	06/2015 -	03/2020	57(O) -	36/36
108	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA ,	07/2012	417.33 -	384.32	115.04	07/2016 -	03/2020	44(O) -	26/28
109	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA ,	11/2012	430.45 -	415.37	189.54	03/2016 -	03/2020	48(O) -	38/39
110	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]SCCL,TELANGANA ,	05/2015	397.09 -	442.42	99.56	03/2019 -	03/2020	12(O) -	15/18
111	KOYAGUDEM OPENCAST PROJECT - [N06000146]SCCL,TELANGANA , Central Sector Projects	10/2015	426.79 -	426.79	.72	03/2018 -	03/2020	24(O) -	0/9
112	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]SCCL,TELANGANA ,	12/2015	477.65 -	477.65	2.11	03/2020 -	03/2020	0(O) -	5/17
113	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]SCCL,TELANGANA ,	03/2017	413.84 -	413.84	123.18	03/2019 -	03/2022	36(O) -	1/11
114	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL,TELANGANA ,	11/2016	272.73 -	272.73	153.75	- 04/2017	03/2020	- 0	1/6

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
115	RAMPURAM SHAFT BLOCK - [N06000174]SCCL,TELANGANA ,	08/2016	431.92 -	431.92	.00	- 03/2023	-	-	0/9
116	SRAVANAPALLI OPENCAST PROJECT - [N06000175]SCCL,TELANGANA ,	02/2018	412.70 -	412.70	.76	- 03/2023	-	-	0/7
117	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH ,	07/2016	17,237.00 -	17,237.80	8,596.47	11/2021 -	11/2021	0(O) -	0/0
118	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]ECL,WEST BENGAL ,	11/2015	602.86 -	602.86	318.97	03/2022 -	03/2022	0(O) -	9/13
119	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL ,	08/2012	1,055.05 -	1,055.05	562.60	03/2018 -	10/2020	31(O) -	11/16
120	RANIGANJ MASTER PLAN - [N06000163]ECL,WEST BENGAL ,	08/2009	2,661.73 -	5,146.48	364.72	08/2019 -	08/2024	60(O) -	0/19
121	SIDULI MINE (OC AND UG) - [N06000165]ECL,WEST BENGAL ,	05/2018	535.18 -	535.18	.19	03/2026 -	03/2026	0(O) -	1/22
122	NAKRAKONDA KUMARDIH B OCP - [N06000170]ECL,WEST BENGAL ,	08/2018	502.68 -	502.68	.00	03/2029 -	03/2029	0(O) -	0/22
123	TILABONI UG MINE - [N06000172]ECL,WEST BENGAL ,	02/2019	916.62 -	916.62	.00	03/2027 -	03/2027	0(O) -	0/27
124	PARASEA- BELBAID REORGANISATION UG MINE - [N06000185]ECL,WEST BENGAL ,	07/2019	826.42 -	826.42	.00	03/2027 -	03/2027	0(O) -	0/22
	Total		1,04,637.11 -	1,08,558.02	38,613.72				521/1133
	<u>FERTILISERS</u>								
125	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]NFL,HARYANA ,	01/2018	215.92 -	215.92	134.50	11/2019 -	11/2019	-	0/2
126	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]RCF,MAHARASHTRA ,	04/2018	426.72 -	426.72	268.46	04/2020 07/2020	04/2020	0(O) 0	2/14
127	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]NFL,PUNJAB ,	01/2018	218.83 -	218.83	142.01	11/2019 -	05/2020	6(O) -	0/2
128	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]NFL,PUNJAB ,	01/2018	239.81 -	239.81	156.70	11/2019 -	05/2020	6(O) -	0/2
	Total		1,101.28 -	1,101.28	701.67				2/20
	<u>MINES</u>								
129	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]NALCO,ODISHA ,	12/2014	5,540.00 5,540.00	5,540.00	131.22	04/2021 12/2022	12/2022	20(O) 0	3/4
130	UTKAL D AND E COAL BLOCK - [N10000011]NALCO,ODISHA ,	05/2016	534.00 -	534.00	320.63	01/2020 -	01/2020	0(O) -	1/3
131	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]NALCO,ODISHA , Central Sector Projects	12/2015	355.00 -	355.00	85.98	11/2020 -	11/2020	0(O) -	2/3
132	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]NALCO,ODISHA , Central Sector Projects	11/2017	483.00 483.00	483.00	.48	04/2021 04/2021	04/2021	0(O) 0	2/2

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
133	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]NALCO,TAMIL NADU ,	09/2017	166.62 163.17	163.17	135.00	06/2019 12/2020	12/2020	18(O) 0	1/1
	Total		7,078.62 -	7,075.17	673.31				9/13
	<u>STEEL</u>								
134	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH ,	12/2011	2,858.00 -	2,500.00	1,535.76	12/2017 03/2020	03/2020	27(O) 2	5/6
135	CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH ,	08/2015	320.66 -	320.66	257.04	08/2018 02/2020	02/2020	18(O) 1	3/4
136	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH ,	01/2010	15,525.00 23,140.00	23,140.00	16,468.33	05/2015 07/2020	07/2020	62(O) 0	66/86
137	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND ,	03/2015	1,034.01 -	1,034.01	450.11	10/2017 06/2020	06/2020	32(O) 0	0/2
138	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND ,	05/2015	1,154.18 -	1,154.18	998.53	12/2017 01/2020	03/2020	27(O) 2	2/2
139	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND ,	11/2016	262.87 -	262.87	131.30	06/2019 06/2020	11/2020	17(O) 5	0/1
140	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA ,	04/2015	3,127.30 -	3,127.30	3,201.42	04/2018 01/2020	01/2020	21(O) 0	3/3
141	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH ,	04/2014	1,682.85 -	1,682.85	1,341.85	09/2018 02/2020	02/2020	17(O) 1	4/5
142	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E - [N12000121]SAIL,WEST BENGAL ,	12/2018	263.36 -	263.36	29.03	09/2020 -	09/2020	0(O) -	0/4
	Total		26,228.23 -	33,485.23	24,413.37				83/113
	<u>PETROLEUM</u>								
143	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH ,	07/2016	20,928.00 26,264.00	26,264.00	8,584.07	07/2020 07/2022	07/2022	24(O) 0	89/111
144	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH ,	03/2016	34,012.00 -	34,012.00	4,995.31	06/2020 -	08/2021	14(O) -	15/20
145	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL,ANDHRA PRADESH ,	01/2015	342.00 -	342.00	.00	03/2021 -	03/2021	0(O) -	0/0
146	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL,ANDHRA PRADESH ,	07/2014	247.00 -	247.00	.00	03/2021 -	03/2021	0(O) -	0/0
147	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL AP - [N16000302]IOCL,ANDHRA PRADESH ,	08/2017	384.58 -	384.58	134.67	04/2021 -	09/2020	-7(O) -	0/0
148	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH ,	08/2018	466.00 -	466.00	124.36	04/2021 -	07/2021	3(O) -	0/0
149	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH ,	04/2018	355.00 -	355.00	29.38	04/2022 -	02/2023	10(O) -	0/0
150	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]IOCL,ANDHRA PRADESH ,	10/2018	316.20 -	316.20	18.83	10/2021 -	10/2021	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
151	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364]BPCL,ANDHRA PRADESH ,	07/2017	580.20 -	580.20	66.56	02/2021 -	02/2021	0(O) -	0/16
152	SWRO II WITH LLPH FACILITIES - [N16000378]HPCL,ANDHRA PRADESH ,	09/2019	196.26 -	196.26	.00	07/2020 -	07/2020	0(O) -	0/0
153	LPG BP PROJECT CHITTOOR - [N16000381]IOCL,ANDHRA PRADESH ,	07/2019	167.00 -	167.00	3.62	07/2022 -	07/2022	0(O) -	0/0
154	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) CACHAR ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM ,	06/2016	423.00 -	423.00	363.66	08/2019 -	12/2020	16(O) -	6/13
155	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]IOCL,ASSAM ,	02/2016	2,582.00 -	2,582.00	1,704.47	11/2019 -	02/2020	3(O) -	17/17
156	PIPELINE NETWORK PROJECT GELEKI ASSAM - [N16000278]ONGC,ASSAM ,	07/2016	249.85 265.49	265.49	152.67	05/2020 -	05/2020	0(O) -	4/5
157	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM ,	07/2011	350.00 -	350.00	2.06	01/2019 -	-	-	0/0
158	BS-VI PROJECT AT BONGAIGAON REFINERY - [N16000320]IOCL,ASSAM ,	05/2018	1,222.00 -	1,222.00	739.04	09/2019 -	02/2020	5(O) -	7/7
159	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM ,	01/2018	543.91 -	682.90	71.46	02/2020 -	06/2020	4(O) -	1/14
160	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]IOCL,ASSAM ,	08/2018	557.00 -	557.00	313.62	02/2020 -	04/2020	2(O) -	5/5
161	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CCGS MADHUBAN - [N16000356]OIL,ASSAM ,	06/2016	224.75 -	224.75	98.98	08/2020 -	08/2020	0(O) -	0/0
162	NUMALIGARH REFINERY EXPANSION PROJECT - [N16000379]NRL,ASSAM ,	01/2019	22,594.00 -	22,594.00	43.00	10/2024 -	10/2024	0(O) -	0/0
163	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM ,	09/2012	871.35 -	1,200.00	565.63	03/2015 -	-	-	0/5
164	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]IOCL,BIHAR ,	05/2016	664.00 -	729.40	664.73	12/2020 -	02/2020	-10(O) -	4/5
165	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]IOCL,BIHAR ,	09/2015	324.00 -	324.00	199.72	06/2020 -	03/2020	-3(O) -	3/4
166	LPG BP PROJECT MOTIHARI - [N16000317]IOCL,BIHAR ,	05/2018	206.50 -	206.50	38.09	03/2021 -	03/2021	0(O) -	17/26
167	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]IOCL,BIHAR ,	12/2017	199.36 -	199.36	9.39	10/2020 -	10/2020	0(O) -	2/2
168	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]GAIL,BIHAR ,	10/2017	359.25 -	359.25	81.40	10/2022 -	10/2022	0(O) -	8/10
169	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]IOCL,BIHAR ,	07/2018	189.00 -	189.00	33.25	01/2021 -	01/2021	0(O) -	4/8
170	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI BIHAR - [N16000344]IOCL,BIHAR ,	04/2018	522.00 -	522.00	187.36	03/2021 -	03/2021	0(O) -	0/0
171	FUEL QUALITY UPGRADATION (NSU NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY - [N16000348]IOCL,BIHAR ,	06/2017	951.64 -	951.64	552.00	10/2019 -	05/2020	7(O) -	9/11
172	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI ,	08/2014	6,086.08 5,842.31	5,842.31	4,784.88	05/2019 03/2020	03/2020	10(O) 5	13/14
173	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT ,	04/2016	327.78 -	200.00	155.59	04/2018 -	02/2020	22(O) -	18/20

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
174	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]ONGC,GUJARAT ,	02/2017	1,162.56 -	1,162.56	441.61	03/2026 -	03/2026	0(O) -	7/10
175	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]IOCL,GUJARAT , Central Sector Projects	09/2016	208.35 -	208.35	148.25	07/2020 -	07/2020	0(O) -	10/10
176	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309]IOCL,GUJARAT ,	08/2017	1,342.00 -	1,342.00	6.30	08/2020 -	08/2020	0(O) -	1/1
177	BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]IOCL,GUJARAT ,	03/2018	3,380.00 -	3,380.00	2,346.62	09/2019 -	02/2020	5(O) -	9/9
178	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT ,	10/2017	906.00 -	906.00	123.94	02/2020 -	10/2020	8(O) -	4/8
179	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA GUJARAT - [N16000336]IOCL,GUJARAT ,	03/2018	588.20 -	588.20	1.24	- -	08/2022	- -	9/17
180	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]GAIL,GUJARAT ,	09/2018	225.54 -	225.54	2.44	02/2021 -	02/2021	0(O) -	3/8
181	LAB REVAMP AT GUJARAT REFINERY - [N16000377]IOCL,GUJARAT , Central Sector Projects	10/2019	403.00 -	403.00	43.50	12/2021 -	12/2021	0(O) -	0/0
182	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY - [N16000382]IOCL,GUJARAT ,	11/2019	5,251.00 -	5,251.00	.00	05/2023 -	05/2023	0(O) -	0/0
183	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]HPCL,HARYANA ,	11/2017	255.00 -	255.00	128.36	11/2020 -	11/2020	0(O) -	26/46
184	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]IOCL,HARYANA ,	04/2018	206.63 -	206.63	29.25	02/2020 -	12/2020	10(O) -	5/6
185	BS-VI PROJECT AT PANIPAT REFINERY - [N16000325]IOCL,HARYANA ,	12/2017	3,529.00 -	3,529.00	2,088.18	07/2019 -	02/2020	7(O) -	9/9
186	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]IOCL,HARYANA ,	08/2018	1,636.00 -	1,636.00	160.86	08/2020 -	08/2020	0(O) -	5/6
187	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]IOCL,HARYANA ,	01/2019	909.00 -	909.00	23.71	01/2021 -	08/2021	7(O) -	0/0
188	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]IOCL,HARYANA ,	10/2018	598.00 -	598.00	27.18	02/2020 -	01/2021	11(O) -	4/4
189	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]GAIL,HARYANA ,	08/2018	286.42 -	286.42	6.18	08/2020 09/2020	09/2020	1(O) 0	11/16
190	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV PANIPAT - [N16000363]IOCL,HARYANA ,	12/2018	278.60 -	278.60	.00	06/2021 -	06/2021	0(O) -	1/3
191	R and D CAMPUS II AT FARIDABAD - [N16000375]IOCL,HARYANA ,	06/2019	2,281.94 -	2,281.94	.00	12/2022 -	12/2022	0(O) -	0/0
192	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]IOCL,HARYANA ,	08/2019	1,255.00 -	1,255.00	106.50	10/2021 -	10/2021	0(O) -	0/0
193	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383]IOCL,HARYANA ,	09/2019	164.69 -	164.69	.00	07/2021 -	07/2021	0(O) -	0/0
194	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]ONGC,JHARKHAND ,	12/2015	823.27 910.23	910.23	441.81	03/2023 03/2022	03/2022	-12(O) 0	6/10
195	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]HPCL,JHARKHAND ,	06/2017	161.50 -	161.50	17.78	06/2020 -	09/2021	15(O) -	0/12

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
196	CITY GAS DISTRIBUTION (CGD) NETWORK RANCHI - [N16000329]GAIL,JHARKHAND ,	10/2017	226.45 -	226.45	62.72	10/2022 -	10/2022	0(O) -	12/17
197	CITY GAS DISTRIBUTION (CGD) NETWORK JAMSHEDPUR - [N16000330]GAIL,JHARKHAND ,	10/2017	221.45 -	221.45	52.67	10/2022 -	10/2022	0(O) -	6/9
198	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]BPCL,JHARKHAND ,	11/2018	248.55 -	248.55	29.20	06/2022 -	06/2022	0(O) -	0/0
199	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRIL,KARNATAKA ,	01/2006	993.00 -	1,693.00	1,549.85	01/2012 -	-	-	0/0
200	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA , Central Sector Projects	02/2015	749.00 -	842.00	606.89	02/2020 -	02/2020	0(O) -	0/0
201	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]MANGALORE REFIN,KARNATAKA ,	05/2015	224.00 207.00	185.00	164.61	04/2019 -	-	-	8/8
202	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]MANGALORE REFIN,KARNATAKA ,	10/2015	135.00 171.00	170.70	156.65	03/2019 -	-	-	11/11
203	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA ,	09/2016	1,810.00 1,810.00	1,810.00	1,022.88	12/2019 07/2020	03/2021	15(O) 0	8/9
204	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA , Central Sector Projects	11/2017	581.00 -	621.00	154.66	03/2020 11/2020	11/2020	8(O) 0	2/3
205	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]BPCL,KARNATAKA ,	10/2018	206.26 -	206.26	13.42	03/2021 -	03/2021	0(O) -	0/15
206	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367]HPCL,KARNATAKA ,	06/2019	2,166.38 -	2,166.38	33.41	06/2022 -	06/2022	0(O) -	2/18
207	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369]HPCL,KARNATAKA ,	12/2018	854.00 -	854.00	56.18	12/2022 -	12/2022	0(O) -	9/19
208	SETTING UP OF PHASE LL FACILITIES FOR HPCL GREEN R AND D CENTRE AT BENGALURU - [N16000380]HPCL,KARNATAKA ,	06/2018	380.00 -	380.00	82.70	11/2021 -	11/2021	0(O) -	7/19
209	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA ,	10/2015	607.06 -	714.25	356.62	10/2017 -	-	-	39/52
210	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA ,	11/2014	4,588.29 5,245.96	5,245.96	4,137.20	08/2018 11/2019	02/2020	18(O) 2	0/20
211	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA ,	02/2016	3,313.00 3,288.96	3,288.96	1,673.55	02/2020 10/2020	10/2020	8(O) 0	0/20
212	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA ,	12/2015	1,112.00 1,507.24	1,507.24	566.00	06/2019 02/2022	02/2022	32(O) 0	0/0
213	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]BPCL,KERALA ,	09/2018	11,130.00 -	11,130.00	89.09	03/2023 -	03/2023	0(O) -	0/0
214	PROVISION OF 2ND SPUR FOR TWL GANTRY TWD FACILITY FOR MS AND HSD ADDITIONAL TANKS FOR MS HSD AND - [N16000304]IOCL,MADHYA PRADESH ,	08/2017	236.00 -	236.00	49.62	06/2020 -	10/2020	4(O) -	0/0
215	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA ,	03/2011	861.79 -	1,683.06	1,386.15	05/2013 02/2020	02/2020	81(O) 2	4/8
216	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA ,	12/2011	2,059.63 2,665.65	2,665.65	1,933.09	03/2015 03/2020	03/2020	60(O) 3	15/18

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
217	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA ,	11/2014	6,068.80 -	5,296.93	4,845.91	04/2019 03/2020	03/2020	11(O) 3	8/9
218	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA ,	08/2015	2,818.88 -	2,818.88	2,401.67	03/2019 05/2020	05/2020	14(O) 0	4/5
219	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA BASSEIN AND PANNA - [N16000212]ONGC,MAHARASHTRA , Central Sector Projects	01/2015	4,619.94 -	4,619.94	4,586.11	12/2017 03/2020	03/2020	27(O) 0	4/5
220	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA , Central Sector Projects	12/2015	3,190.69 -	3,247.19	2,369.08	04/2018 05/2020	05/2020	25(O) 0	13/15
221	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL,MAHARASHTRA ,	05/2016	1,945.00 -	1,945.00	1,074.02	08/2021 -	08/2021	0(O) -	5/5
222	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]BPCL,MAHARASHTRA ,	02/2016	554.00 -	554.00	375.80	02/2020 -	02/2020	0(O) -	0/10
223	MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL,MAHARASHTRA ,	04/2013	449.58 -	449.58	215.10	12/2019 07/2020	07/2020	7(O) 0	0/17
224	ADDITIONAL FACILITIES AT MANMAD FOR COVERSON TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA ,	05/2016	212.00 -	212.00	57.97	01/2021 -	04/2021	3(O) -	0/0
225	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA ,	05/2016	348.00 -	348.00	101.41	01/2021 -	10/2021	9(O) -	0/0
226	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL,MAHARASHTRA ,	05/2016	261.00 -	261.00	71.13	01/2021 -	01/2021	0(O) -	0/0
227	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL,MAHARASHTRA ,	09/2015	4,199.00 5,060.00	5,060.00	3,446.40	03/2020 -	03/2020	0(O) -	112/135
228	DEVELOPMENT OF B-147 FIELD - [N16000292]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	546.15 565.15	565.15	468.71	11/2019 03/2020	03/2020	4(O) 0	4/5
229	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]ONGC,MAHARASHTRA ,	02/2017	4,006.83 -	4,475.92	2,975.26	05/2021 12/2021	12/2021	7(O) 0	11/15
230	PUNE POL STORAGE DEPOT - [N16000313]BPCL,MAHARASHTRA ,	08/2016	282.64 -	282.64	164.77	08/2020 -	08/2020	0(O) -	0/15
231	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD) MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA ,	06/2017	249.26 -	249.26	62.55	06/2020 -	09/2021	15(O) -	0/12
232	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) - [N16000335]ONGC,MAHARASHTRA ,	04/2018	766.37 -	766.37	481.94	12/2019 03/2020	03/2020	3(O) 3	4/5
233	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3 D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]ONGC,MAHARASHTRA ,	02/2019	2,292.46 -	2,292.46	815.60	05/2021 -	05/2021	0(O) -	4/6
234	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]ONGC,MAHARASHTRA ,	04/2019	3,228.80 -	3,228.80	510.66	03/2022 -	03/2022	0(O) -	4/6
235	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]ONGC,MAHARASHTRA ,	02/2019	3,660.71 3,740.05	3,740.05	373.79	04/2021 -	05/2021	1(O) -	4/6

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
236	HEERA REDEVELOPMENT - PHASE III - [N16000360]ONGC,MAHARASHTRA ,	05/2019	2,494.68 -	2,494.68	270.26	12/2021 -	03/2022	3(O) -	4/6
237	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]ONGC,MAHARASHTRA ,	05/2019	763.92 -	763.92	205.99	12/2020 -	12/2020	0(O) -	4/5
238	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE ,	07/2011	352.56 -	438.84	268.45	03/2017 06/2020	06/2020	39(O) 0	2/15
239	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE ,	01/2015	1,823.00 3,027.90	3,027.90	1,030.43	12/2020 -	12/2020	0(O) -	4/5
240	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE ,	01/2015	2,321.00 3,338.00	3,338.00	2,123.21	12/2020 -	08/2020	-4(O) -	4/5
241	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE ,	01/2015	690.00 -	690.00	351.04	07/2018 -	10/2020	27(O) -	24/36
242	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]HPCL,MULTI STATE ,	09/2016	1,879.00 -	1,879.00	1,590.22	06/2020 -	06/2020	0(O) -	24/24
243	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE ,	05/2016	406.00 -	406.00	106.50	10/2020 -	10/2020	0(O) -	6/12
244	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE ,	09/2016	571.66 -	571.66	372.70	12/2019 06/2020	06/2020	6(O) 0	6/22
245	LAYING OF VIJAIPIUR-AURAIYA PIPELINE SECTION OF VIJAIPIUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE ,	07/2015	2,881.40 -	2,000.00	1,326.88	12/2020 -	12/2020	0(O) -	19/24
246	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]GAIL,MULTI STATE ,	03/2017	2,433.00 -	2,433.00	1,566.59	12/2020 -	12/2020	0(O) -	18/24
247	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]GAIL,MULTI STATE ,	03/2017	3,437.00 -	3,437.00	1,326.48	12/2020 -	12/2020	0(O) -	18/24
248	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE , Central Sector Projects	06/2009	2,915.00 4,915.00	4,915.00	2,784.58	12/2012 02/2022	02/2022	110(O) 0	25/42
249	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]HPCL,MULTI STATE ,	09/2017	2,677.00 -	2,677.00	1,106.90	03/2021 -	03/2021	0(O) -	13/26
250	50MW WIND ENERGY POWER PROJECT - [N16000298]OIL,MULTI STATE ,	11/2015	500.00 -	500.00	.00	06/2017 -	-	-	0/0
251	BARAUNI-GUWAHATI PIPELINE - [N16000334]GAIL,MULTI STATE ,	06/2018	3,308.00 -	3,308.00	1,433.56	12/2021 -	12/2021	0(O) -	11/20
252	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]GAIL,ODISHA ,	03/2017	1,933.00 -	1,933.00	1,068.40	12/2020 -	12/2020	0(O) -	18/24
253	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]IOCL,ODISHA ,	05/2016	429.00 -	429.00	329.59	01/2019 -	06/2020	17(O) -	6/6
254	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA , Central Sector Projects	12/2016	161.59 -	161.59	40.21	12/2019 -	07/2021	19(O) -	17/26
255	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL,ODISHA , Central Sector Projects	07/2017	243.53 -	243.53	58.94	07/2022 -	07/2022	0(O) -	6/10
256	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]IOCL,ODISHA ,	08/2017	315.00 -	315.00	124.98	12/2021 -	12/2020	-12(O) -	2/3

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
257	CITY GAS DISTRIBUTION (CGD) NETWORK CUTTACK - [N16000328]GAIL, ODISHA ,	07/2017	182.20 -	182.20	34.88	07/2022 -	07/2022	0(O) -	5/9
258	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]IOCL, ODISHA ,	04/2018	5,654.00 -	5,654.00	686.68	10/2021 -	10/2021	0(O) -	4/10
259	2G ETHANOL BIO REFINERY AT BARGARH - [N16000341]BPCL, ODISHA ,	08/2017	750.00 -	750.00	34.73	12/2020 -	12/2020	0(O) -	0/14
260	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]IOCL, ODISHA ,	10/2018	1,297.50 -	1,297.50	30.00	10/2021 -	10/2021	0(O) -	1/1
261	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]IOCL, ODISHA ,	11/2018	462.30 -	462.30	.00	09/2021 -	09/2021	0(O) -	0/0
262	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]IOCL, ODISHA ,	05/2019	3,361.00 -	3,361.00	468.48	08/2021 -	08/2021	0(O) -	5/11
263	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]IOCL, ODISHA ,	06/2019	371.00 -	371.00	.00	09/2022 -	09/2022	0(O) -	0/0
264	2ND GENERATION LIGNOCELLUOSIC BIOMASS ETHANOL BIOFUEL REFINERY AT BARGARH (ODISHA) - [N16000374]BPCL, ODISHA ,	08/2019	1,607.00 -	1,607.00	40.99	08/2022 -	08/2022	0(O) -	0/21
265	LPG BP PROJECT JODHPUR - [N16000318]IOCL, RAJASTHAN ,	03/2018	229.80 -	229.80	74.47	-	03/2021	-	13/26
266	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL, TAMIL NADU ,	05/2013	711.00 -	711.00	11.12	06/2020 -	06/2020	0(O) -	0/0
267	RESID UPGRADATION PROJECT - [N16000184]CPCL, TAMIL NADU ,	03/2013	3,110.36 -	3,110.36	2,915.00	11/2015 -	-	-	52/52
268	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL, TAMIL NADU ,	11/2012	678.00 -	678.00	8.10	02/2017 -	10/2021	56(O) -	0/0
269	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC, TAMIL NADU ,	11/2015	650.82 -	650.82	432.28	03/2019 05/2020	05/2020	14(O) 0	4/5
270	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL, TAMIL NADU ,	05/2016	4,497.00 6,025.00	6,025.00	1,588.02	12/2018 -	02/2021	26(O) -	4/5
271	AUGMENTATION OF CTMPL - [N16000286]IOCL, TAMIL NADU , Central Sector Projects	12/2016	228.00 -	228.00	36.09	06/2020 -	06/2020	0(O) -	4/5
272	BS-VI PROJECTS - [N16000295]CPCL, TAMIL NADU ,	09/2017	1,858.00 -	1,858.00	1,229.51	12/2019 -	04/2020	4(O) -	0/0
273	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL, TAMIL NADU ,	08/2017	421.00 -	421.00	177.80	08/2020 -	02/2021	6(O) -	0/0
274	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR TAMIL NADU - [N16000305]IOCL, TAMIL NADU ,	12/2017	466.43 -	466.43	68.41	10/2020 -	08/2021	10(O) -	0/0
275	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL, TELANGANA ,	12/2018	611.00 -	611.00	13.32	04/2022 -	03/2023	11(O) -	0/0
276	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]GAIL, UTTAR PRADESH , Central Sector Projects	04/2017	287.49 -	287.49	138.25	04/2022 -	04/2022	0(O) -	39/43
277	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL, UTTAR PRADESH ,	08/2017	318.80 -	318.80	63.90	08/2021 -	11/2021	3(O) -	0/0
278	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]IOCL, UTTAR PRADESH ,	01/2018	666.64 -	666.64	493.90	09/2019 -	01/2020	4(O) -	6/6
279	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]IOCL, UTTAR PRADESH ,	08/2017	255.40 -	255.40	6.53	08/2020 -	08/2020	0(O) -	1/1

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
280	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]IOCL,UTTAR PRADESH ,	03/2018	676.00 -	676.00	271.05	12/2021 -	12/2021	0(O) -	2/3
281	120 TMTA LPG BOTTLING PLANT AT GORAKHPUR UP - [N16000354]IOCL,UTTAR PRADESH ,	03/2014	204.00 -	204.00	148.58	09/2019 -	-	-	6/6
282	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL - [N16000365]BPCL,UTTAR PRADESH ,	12/2017	1,524.06 -	1,524.06	22.01	12/2021 -	12/2021	0(O) -	0/21
283	REDEVELOPMENT/ EXPANSION OF MEERUT DEPOT FOR ENHANCING PRODUCT HANDLING CAPACITY - [N16000366]HPCL,UTTAR PRADESH ,	08/2016	154.84 -	154.84	128.71	11/2019 -	11/2019	-	40/40
284	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND , Central Sector Projects	02/2017	160.10 -	160.10	54.94	02/2020 -	10/2020	8(O) -	18/26
285	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL,WEST BENGAL ,	03/2015	694.00 1,097.54	1,097.54	856.34	10/2018 02/2020	02/2020	16(O) 0	0/15
286	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL,WEST BENGAL ,	04/2016	1,021.00 -	1,021.00	4.45	12/2020 -	12/2020	0(O) -	0/0
287	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]GAIL,WEST BENGAL ,	03/2017	1,740.00 -	1,740.00	612.62	12/2020 -	12/2020	0(O) -	13/24
288	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL,WEST BENGAL ,	04/2017	163.02 -	163.02	59.14	04/2020 -	03/2021	11(O) -	17/26
289	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY - [N16000322]IOCL,WEST BENGAL ,	05/2018	2,934.40 -	2,934.40	1,928.10	09/2019 -	02/2020	5(O) -	11/11
290	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]IOCL,WEST BENGAL ,	03/2018	3,712.00 -	3,696.00	1,001.53	09/2022 -	06/2021	-15(O) -	1/3
	Total		2,69,889.88 -	2,84,938.40	1,01,562.39				1109/1748
	<u>POWER</u>								
291	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH ,	09/2003	6,285.33 -	19,496.34	11,842.12	09/2010 08/2023	08/2023	155(O) 0	0/0
292	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH ,	12/2004	2,496.90 7,927.34	7,927.34	7,743.76	12/2009 06/2020	06/2020	126(O) 5	30/30
293	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR ,	02/2005	8,692.97 21,312.11	21,312.11	16,928.07	10/2011 08/2021	08/2021	118(O) 0	30/47
294	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR ,	01/2007	5,353.00 7,998.00	9,583.00	8,056.25	07/2012 -	09/2020	98(O) -	12/25
295	NPCCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR , Joint Venture	01/2013	12,964.60 17,304.00	17,304.00	14,367.00	05/2018 12/2021	06/2021	37(O) 0	36/45
296	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]SJVN,BIHAR ,	03/2019	10,439.09 10,439.09	10,439.09	876.79	01/2024 -	01/2024	0(O) -	16/19
297	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH ,	12/2012	11,846.00 -	12,739.82	12,826.56	10/2017 03/2020	03/2020	29(O) 0	38/41
298	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH ,	09/2015	3,004.00 -	3,004.00	1,813.00	11/2019 -	11/2019	-	0/0
299	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI ,	03/2015	1,394.52 -	1,394.52	457.17	05/2017 06/2019	03/2020	34(O) 0	4/9

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
300	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL, GUJARAT , Central Sector Projects	05/2017	175.64 -	175.64	106.20	09/2018 03/2020	03/2020	18(O) 0	0/0
301	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL, GUJARAT ,	12/2017	193.14 -	193.14	102.44	06/2019 03/2020	03/2020	9(O) 0	0/0
302	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC, HIMACHAL PRADESH ,	09/2002	3,919.59 -	9,997.11	7,761.19	09/2009 12/2021	12/2021	147(O) 0	3/5
303	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC, JHARKHAND ,	02/2014	14,366.58 -	15,164.05	9,965.78	06/2019 09/2019	03/2022	33(O) 0	25/30
304	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC, JHARKHAND ,	10/2004	4,237.96 4,238.00	4,552.00	3,365.00	10/2017 -	-	-	0/0
305	PATRATU STPP-I (3X800MW) - [N18000275]NTPC, JHARKHAND ,	11/2017	18,668.00 -	18,668.00	2,409.34	03/2023 -	03/2023	0(O) -	2/2
306	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL, KARNATAKA , Central Sector Projects	05/2017	445.89 -	445.89	332.46	02/2019 12/2019	05/2020	15(O) 2	0/0
307	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC, MADHYA PRADESH ,	03/2013	11,638.55 -	12,865.92	12,503.29	01/2018 03/2020	03/2020	26(O) 0	40/42
308	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC, MADHYA PRADESH ,	03/2015	9,870.51 -	11,148.86	9,430.15	01/2020 -	02/2020	1(O) -	40/41
309	AMELIA COAL MINE - [N18000252]THDCIL, MADHYA PRADESH , Central Sector Projects	01/2017	2,104.21 -	1,587.16	309.90	09/2020 -	09/2020	0(O) -	9/16
310	MOUDA STPP STAGE 2 - [N18000132]NTPC, MAHARASHTRA ,	03/2012	7,921.47 -	7,921.47	5,302.00	09/2016 -	-	-	41/41
311	LOKTAK D/S HEP (NHPC) - [180100078]NHPC, MANIPUR ,	12/1999	578.62 -	578.62	.00	06/2006 -	-	-	0/0
312	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL, MULTI STATE ,	10/2008	4,824.12 5,071.94	5,071.94	4,595.36	10/2012 12/2019	03/2020	89(O) 0	8/11
313	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL, MULTI STATE ,	02/2009	11,130.19 14,719.10	14,719.10	12,824.45	08/2013 03/2022	03/2022	103(O) 0	23/26
314	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL, MULTI STATE ,	10/2011	487.49 639.46	639.46	590.30	06/2014 09/2019	02/2020	68(O) 1	10/12
315	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL, MULTI STATE ,	10/2013	1,364.52 1,891.41	1,891.41	1,283.60	04/2016 08/2019	02/2020	46(O) 1	8/12
316	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL, MULTI STATE ,	01/2014	374.63 374.63	374.63	224.83	04/2016 12/2017	03/2020	47(O) 0	0/0
317	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL, MULTI STATE ,	05/2014	522.29 546.36	546.36	470.71	11/2016 06/2020	03/2020	40(O) 0	8/12
318	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL, MULTI STATE ,	06/2014	5,151.37 5,151.37	5,151.37	3,269.93	03/2018 12/2019	03/2020	24(O) 1	9/12
319	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL, MULTI STATE ,	01/2015	871.62 -	871.62	606.81	10/2017 09/2019	03/2020	29(O) 0	0/5
320	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL, MULTI STATE ,	01/2015	203.28 260.03	260.03	200.16	07/2017 06/2019	01/2020	30(O) 0	3/5

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
321	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE ,	03/2015	197.40 197.40	197.40	85.34	03/2018 -	03/2020	24(O) -	0/0
322	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE ,	03/2016	808.63 -	808.63	547.80	01/2018 03/2020	03/2020	26(O) 0	0/0
323	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE ,	05/2016	3,519.59 -	3,519.59	2,562.41	05/2019 -	02/2020	9(O) -	0/0
324	HVDC BIPOLE LINK BETWEEN WR (RAIGARH CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE ,	05/2016	14,733.37 -	14,733.37	9,883.31	11/2019 -	03/2020	4(O) -	0/0
325	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE ,	03/2017	283.72 -	283.72	196.10	11/2019 -	11/2019	-	0/0
326	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE ,	10/2016	408.46 -	408.46	322.79	01/2019 09/2019	03/2020	14(O) 0	0/0
327	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE ,	10/2016	608.24 -	608.24	425.04	04/2019 -	01/2020	9(O) -	0/0
328	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/- [N18000242]PGCIL,MULTI STATE ,	02/2017	322.30 -	322.30	166.84	02/2019 04/2020	03/2020	13(O) 0	0/0
329	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE ,	02/2017	235.53 -	235.53	138.98	06/2019 -	03/2020	9(O) -	0/0
330	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE ,	03/2017	379.95 -	379.95	113.54	12/2019 -	03/2020	3(O) -	0/0
331	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH CHATTISGARH) AND SOUTHERN REGION (PUGALAR TM) NOR - [N18000247]PGCIL,MULTI STATE ,	02/2017	5,070.13 -	5,070.13	3,270.48	04/2020 -	04/2020	0(O) -	0/0
332	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE ,	12/2014	4,754.42 -	9,072.36	1,402.48	12/2018 -	12/2020	24(O) -	0/0
333	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE ,	12/2014	5,111.33 -	6,880.36	1,886.30	12/2018 -	12/2020	24(O) -	0/0
334	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE , Central Sector Projects	12/2015	3,654.00 -	3,654.00	3,508.04	04/2019 -	01/2020	9(O) -	0/0
335	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE , Central Sector Projects	03/2017	3,500.00 3,500.00	3,500.00	2,039.35	07/2020 -	07/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
336	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE , Central Sector Projects	08/2017	1,931.39 -	1,931.39	1,164.36	02/2020 -	06/2020	4(O) -	0/0
337	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE ,	09/2017	198.49 -	198.49	126.26	09/2019 02/2020	02/2020	5(O) 0	0/0
338	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE ,	11/2017	358.83 -	358.83	177.36	05/2020 -	05/2020	0(O) -	0/0
339	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA ,	02/2014	12,532.44 -	13,740.53	10,182.96	12/2018 02/2020	08/2020	20(O) 2	37/41
340	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC,ODISHA ,	05/2016	1,885.13 -	1,885.13	1,486.29	12/2018 -	08/2020	20(O) -	0/0
341	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU , Central Sector Projects	05/2017	186.17 -	186.17	111.47	07/2019 -	03/2020	8(O) -	0/0
342	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA ,	01/2016	10,598.98 -	10,598.98	6,325.54	11/2020 02/2021	09/2021	10(O) 3	24/26
343	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH ,	09/2014	9,188.98 -	10,016.10	7,036.74	07/2019 03/2020	09/2020	14(O) 0	36/40
344	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH , Joint Venture	04/2012	9,750.89 -	12,176.28	10,103.00	02/2017 06/2020	06/2020	40(O) 0	37/40
345	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH ,	03/2019	11,089.42 -	11,089.42	909.73	09/2023 -	09/2023	0(O) -	0/0
346	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000273]NTPC,UTTAR PRADESH ,	12/2018	587.44 -	587.44	250.00	09/2020 -	09/2020	0(O) -	0/0
347	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000274]NTPC,UTTAR PRADESH ,	03/2019	349.00 -	349.00	125.00	11/2020 -	11/2020	0(O) -	0/0
348	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND ,	11/2006	2,978.48 5,867.38	5,867.38	4,346.71	03/2013 12/2020	12/2021	105(O) 0	7/15
349	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND ,	08/2008	2,491.58 -	4,397.80	1,858.35	06/2013 -	12/2022	114(O) -	11/13
350	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND ,	07/2012	1,527.00 -	1,801.07	148.93	08/2017 -	-	-	0/15
351	NAITWAR MORI HEP - [N18000265]SJVN,UTTARAKHAND ,	10/2017	648.33 -	648.33	310.91	12/2021 -	12/2021	0(O) -	6/32
352	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL ,	09/2014	1,381.84 -	1,592.34	526.08	09/2019 02/2022	11/2022	38(O) 0	5/9
353	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL ,	04/2016	454.11 -	454.11	297.68	04/2018 01/2020	01/2020	21(O) 0	0/0
354	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC,WEST BENGAL ,	12/2016	529.68 -	529.68	294.18	11/2018 -	08/2020	21(O) -	0/0
	Total		2,73,781.33 -	3,44,106.51	2,22,894.97				558/719
	<u>HEAVY INDUSTRY</u>								
355	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL,DELHI , Central Sector Projects	08/2016	1,554.00 -	1,554.00	716.25	09/2019 -	03/2020	6(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	Total		1,554.00 -	1,554.00	716.25				0/0
	<u>HEALTH AND FAMILY WELFARE</u>								
356	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS-MNAGLAGIRI GUNTUR ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH , Central Sector Projects	08/2017	272.19 -	272.54	204.08	03/2019 -	03/2020	12(O) -	0/0
357	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH , Central Sector Projects	03/2018	601.02 -	601.02	219.05	- -	07/2020	- -	0/0
358	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI ASSAM - [N21000027]HITES,ASSAM ,	05/2017	875.00 -	747.80	137.27	05/2021 08/2021	10/2021	5(O) 0	0/0
359	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI ,	02/2013	414.11 -	499.23	337.32	11/2013 -	09/2020	82(O) -	0/0
360	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI ,	12/2013	204.44 -	270.00	210.75	05/2017 -	06/2020	37(O) -	2/2
361	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI ,	08/2014	293.65 -	325.00	304.62	05/2017 -	01/2020	32(O) -	3/5
362	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI ,	12/2017	156.56 -	156.64	80.28	- -	05/2020	- -	0/0
363	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA , Central Sector Projects	01/2018	249.01 -	249.07	149.26	- -	05/2020	- -	0/0
364	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA ,	09/2014	505.58 -	585.00	586.96	03/2018 -	09/2019	-	1/2
365	AIIMS BILASPUR - [N21000028]NBCC,HIMACHAL PRADESH ,	04/2018	1,351.00 1,471.00	1,471.00	421.44	09/2021 -	09/2021	0(O) -	0/0
366	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR SAMBA JAMMU AND KASHMIR - [N21000029]CPWD,JAMMU AND KASHMIR ,	03/2019	1,404.00 -	1,404.00	.00	09/2023 -	09/2023	0(O) -	0/0
367	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]CPWD,JAMMU AND KASHMIR ,	03/2019	1,577.00 -	1,828.00	.00	09/2025 -	09/2025	0(O) -	0/0
368	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA , Central Sector Projects	08/2017	274.19 -	274.19	230.83	03/2019 -	03/2020	12(O) -	0/0
369	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA , Central Sector Projects	03/2018	582.99 -	582.99	268.43	- -	06/2020	- -	0/0
370	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA ,	10/2016	363.99 -	363.99	219.50	05/2018 -	07/2020	26(O) -	0/0
371	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB ,	07/2016	152.95 -	177.92	147.31	02/2018 -	03/2020	25(O) -	1/1
372	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA PUNJAB - [N21000026]HITES,PUNJAB ,	07/2016	703.00 -	557.48	327.76	06/2020 -	10/2020	4(O) -	0/0
373	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH , Central Sector Projects	03/2018	268.84 -	268.84	181.36	- -	04/2020	- -	0/0
374	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH ,	07/2016	785.00 -	715.06	385.77	04/2020 -	10/2020	6(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
375	CONSTRUCTION OF HOSPITAL BLOCK IIT KHARAGPUR - [N21000010]HSCC,WEST BENGAL ,	12/2014	168.90 -	191.20	169.51	05/2017 -	07/2019	-	3/3
376	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL ,	08/2016	244.00 -	248.00	224.92	09/2018 -	05/2019	-	0/0
377	RESIDENTIALCOMPLEX AND OPD BLOCK AIIMS KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL , Central Sector Projects	08/2017	355.15 -	355.15	233.51	03/2019 -	07/2020	16(O) -	0/0
378	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC,WEST BENGAL ,	04/2018	651.99 -	651.99	285.33	- -	07/2020	- -	0/0
	Total		12,454.56 -	12,796.11	5,325.26				10/13
	<u>RAILWAYS</u>								
379	NANDYAL-YERRAGUNTLA(NL) SCR - [220100192]SCR,ANDHRA PRADESH ,	03/1996	164.36 -	1,050.00	999.64	02/2009 -	-	-	0/0
380	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH ,	12/2001	1,045.20 2,120.16	2,120.16	561.18	03/2009 -	03/2023	168(O) -	0/0
381	GUDUR-DURGARAJPATNAM - [N22000265]SCR,ANDHRA PRADESH ,	04/2011	761.37 761.37	761.37	.52	- -	-	-	0/0
382	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH ,	04/2013	829.00 829.00	829.00	.94	- -	-	-	1/1
383	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH ,	04/2011	2,288.70 2,643.25	2,643.25	860.07	03/2021 -	03/2024	36(O) -	0/1
384	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH ,	03/2012	1,503.71 -	2,200.00	1,966.03	03/2020 -	03/2022	24(O) -	0/0
385	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH ,	04/2015	3,873.07 3,873.07	3,873.07	.38	- -	-	-	0/0
386	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH ,	04/2016	3,631.00 3,631.00	3,631.00	678.02	03/2022 -	03/2023	12(O) -	0/0
387	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH ,	04/2015	3,246.26 -	3,548.67	1,384.54	12/2023 -	12/2023	0(O) -	0/0
388	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH ,	04/2015	2,499.71 2,499.71	3,382.95	447.56	03/2022 03/2024	03/2024	24(O) 24	0/0
389	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH ,	01/2013	387.70 -	387.70	323.91	03/2018 -	-	-	0/0
390	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH ,	08/2016	234.50 -	235.00	10.88	03/2019 -	12/2020	21(O) -	0/0
391	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT) NEFR - [N22000086]NFR,ASSAM ,	09/2006	385.20 1,532.00	1,532.00	652.15	03/2019 -	03/2020	12(O) -	0/0
392	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM ,	04/2011	314.00 728.00	728.00	731.27	03/2019 -	03/2020	12(O) -	0/0
393	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM ,	04/2015	2,232.32 -	2,182.00	765.94	03/2022 -	03/2020	-24(O) -	0/0
394	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM ,	04/2015	870.96 -	2,136.01	610.95	03/2021 -	03/2021	0(O) -	0/0
395	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC) ECR - [220100240]ECR,BIHAR ,	04/1997	324.73 898.53	1,050.00	1,041.96	03/2012 -	03/2020	96(O) -	0/0
396	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR ,	04/1997	162.87 614.45	614.45	311.33	- -	03/2022	- -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
397	HAJIPUR-SUGAULI VIA VAISHALI (NL) ECR - [220100303]ECR,BIHAR ,	04/2003	528.65 2,066.78	2,066.78	1,454.19	- -	03/2023	- -	0/0
398	KOSI BRIDGE (NL) ECR - [220100304]ECR,BIHAR ,	04/2002	499.41 516.02	516.02	404.10	03/2020 -	03/2020	0(O) -	0/0
399	DANIAWAN-BIHARSARIF (NL) ECR - [220100311]ECR,BIHAR ,	04/2001	406.92 -	339.00	200.00	- -	-	-	0/0
400	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR ,	04/1996	477.88 751.55	751.55	674.58	03/2012 -	03/2020	96(O) -	0/0
401	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) NEFR - [N22000087]NFR,BIHAR ,	09/2006	532.87 2,145.00	2,145.00	935.62	03/2019 -	03/2020	12(O) -	0/0
402	KISHANGANJ JALALGARH NL NEFR - [N22000101]NFR,BIHAR ,	04/2008	333.76 -	360.00	6.74	- 03/2022	03/2022	- 0	0/0
403	ARA-BHABHUA ROAD (NL) - [N22000166]ECR,BIHAR ,	04/2008	633.87 -	633.87	.40	- -	-	-	0/0
404	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR ,	04/2008	620.57 -	620.57	.31	- -	-	-	0/0
405	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR ,	04/2008	445.25 -	445.25	1.15	- -	-	-	0/0
406	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR ,	04/2008	326.20 -	2,995.01	1.94	- -	03/2024	- -	0/0
407	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR ,	04/1999	325.00 735.20	735.20	367.62	- -	03/2021	- -	0/0
408	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR ,	04/2006	378.56 -	1,858.75	377.77	- -	03/2022	- -	0/0
409	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR ,	04/2005	205.00 -	205.00	5.21	- -	-	-	0/0
410	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR ,	04/2006	211.00 -	1,006.00	24.16	- -	-	-	0/0
411	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR ,	04/2008	678.62 -	678.62	17.20	- -	-	-	0/0
412	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR ,	04/2008	228.05 -	228.05	1.53	- -	03/2024	- -	0/0
413	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR ,	04/2008	1,605.17 1,605.17	1,605.17	23.55	- 03/2023	03/2023	- 0	0/0
414	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR ,	04/2008	192.56 -	192.56	.39	- -	-	-	0/0
415	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR ,	04/2008	281.30 -	281.30	.60	- -	-	-	0/0
416	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR ,	04/2004	372.14 1,470.50	1,470.50	849.10	- -	03/2021	- -	0/0
417	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS (NEPAL) GC - [N22000181]ECR,BIHAR ,	04/2009	548.00 819.01	819.01	525.18	03/2020 -	03/2022	24(O) -	0/0
418	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR ,	04/2013	213.01 367.17	440.00	432.20	- -	01/2020	- -	0/1
419	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR ,	05/2015	380.00 519.33	519.33	195.83	- -	02/2023	- -	0/0
420	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR ,	12/2015	1,200.20 1,200.20	1,200.20	586.83	03/2020 -	10/2021	19(O) -	0/1
421	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR ,	12/2015	1,491.47 -	1,491.47	448.67	03/2020 -	12/2021	21(O) -	1/1

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
422	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR ,	01/1991	332.15 546.71	546.71	541.43	07/2014 -	-	-	0/0
423	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR ,	04/2016	744.04 1,215.54	1,215.54	156.95	03/2021 -	03/2022	12(O) -	0/0
424	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR ,	04/2016	731.64 1,185.73	1,185.73	60.65	03/2021 -	03/2022	12(O) -	0/0
425	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR,BIHAR ,	04/1998	180.82 726.31	726.31	521.48	- -	10/2019	-	0/0
426	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA DANIYAWAN-BIHARSHARIF - [N22000476]ECR,BIHAR ,	04/1991	329.39 803.11	1,483.14	1,060.33	- -	12/2021	- -	0/0
427	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH ,	12/2012	1,160.00 1,160.83	1,160.83	749.76	03/2020 03/2023	03/2023	36(O) 0	1/1
428	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH ,	03/2007	1,402.02 -	1,100.00	1,122.87	03/2020 -	12/2020	9(O) -	0/0
429	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH ,	05/2014	207.00 -	207.00	153.83	03/2018 -	-	-	0/0
430	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR,CHHATISGARH ,	04/2008	872.00 1,226.51	1,226.51	1,066.54	12/2019 03/2020	03/2020	3(O) 0	0/0
431	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATISGARH ,	04/2015	1,973.00 1,973.64	1,973.64	185.98	03/2021 03/2023	03/2023	24(O) 0	0/1
432	GEVRA ROAD PENDRA ROAD - [N22000488]IRCON,CHHATISGARH ,	02/2014	2,288.00 -	4,970.11	635.13	03/2022 -	12/2022	9(O) -	0/1
433	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON,CHHATISGARH ,	04/2013	3,055.00 -	3,055.00	2,096.39	09/2018 -	03/2021	30(O) -	0/1
434	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498]RITES,CHHATISGARH ,	02/2016	393.98 -	393.98	290.45	03/2020 -	03/2020	0(O) -	0/2
435	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI ,	04/1999	156.65 -	197.17	106.97	- -	03/2024	- -	0/0
436	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI ,	04/2012	295.68 -	295.68	92.91	- -	03/2023	- -	0/0
437	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT ,	04/2008	829.74 1,215.34	1,310.23	1,532.69	03/2020 03/2021	03/2021	12(O) 0	0/0
438	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT ,	04/2008	318.24 321.62	321.62	125.76	03/2012 03/2022	03/2022	120(O) 0	0/0
439	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT ,	04/2006	117.36 196.95	202.35	809.40	03/2011 -	03/2017	-	0/0
440	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT ,	04/2012	975.62 -	1,082.32	1,202.24	12/2021 -	12/2021	0(O) -	0/0
441	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT ,	04/2012	644.38 -	644.38	507.11	03/2021 -	03/2021	0(O) -	0/0
442	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT ,	04/2011	844.10 844.10	844.10	110.71	- 03/2021	03/2021	- 0	0/0
443	RAJKOT-VERAVAL WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT ,	04/1994	320.66 858.56	858.96	534.00	03/2019 03/2022	03/2022	36(O) 0	0/0
444	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT ,	04/2013	1,548.66 -	1,548.66	1,421.83	12/2021 -	03/2022	3(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
445	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT ,	04/2011	1,037.15 1,037.15	1,037.15	1,035.89	03/2021 03/2022	03/2022	12(O) 0	0/0
446	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT ,	04/2015	1,002.39 1,002.39	1,002.39	454.02	03/2021 03/2021	03/2021	0(O) 0	0/0
447	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT ,	10/2013	343.00 -	343.00	222.83	03/2019 -	-	-	0/0
448	GANDHINAGAR REDEVELOPMENT OF STATION ALO WITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT ,	03/2017	243.60 -	243.60	.00	- -	-	-	0/0
449	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT ,	03/2012	248.26 -	248.26	.00	- -	-	-	0/0
450	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT ,	03/2012	153.83 -	153.83	.00	- -	-	-	0/0
451	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT ,	02/1991	551.51 809.07	809.07	635.52	03/2019 03/2020	03/2020	12(O) 0	0/0
452	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT ,	04/2017	691.84 663.29	663.29	199.24	03/2020 03/2021	03/2021	12(O) 0	0/0
453	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA ,	04/2012	287.00 695.00	750.00	290.62	12/2011 -	03/2021	111(O) -	0/0
454	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA ,	12/2015	346.32 -	346.32	292.82	03/2019 -	03/2020	12(O) -	0/0
455	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH ,	04/2008	2,966.99 -	7,000.00	472.83	12/2026 -	12/2025	-12(O) -	0/0
456	UDHAMPUR-SRINAGAR-BARAMULLA (NL) NR - [220100133]NR,JAMMU AND KASHMIR ,	03/1995	2,500.00 27,949.00	27,949.00	20,501.11	11/2002 -	06/2022	235(O) -	0/0
457	KODERMA-RANCHI VIA BARKAKANA (NL) ECR - [220100222]JECR,JHARKHAND ,	03/1999	1,033.07 3,020.95	3,376.00	3,349.65	- -	03/2021	- -	0/0
458	KODERMA-TILAIYA (NL) ECR - [220100305]JECR,JHARKHAND ,	04/2002	459.91 1,625.87	1,625.87	544.36	- -	03/2021	- -	0/0
459	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND ,	04/2012	258.20 358.68	358.68	278.34	12/2018 12/2018	08/2020	20(O) 2	0/0
460	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND ,	04/2012	148.77 -	377.00	183.96	12/2016 08/2018	03/2020	39(O) 2	0/0
461	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND ,	03/2016	1,724.20 -	1,993.24	469.79	03/2021 03/2021	12/2021	9(O) 0	0/0
462	GARHWA ROAD-RAMNA - [N22000465]JECR,JHARKHAND ,	03/2015	348.23 -	348.23	211.06	03/2021 -	12/2020	-3(O) -	0/0
463	HUBLI-ANKOLA(NL) SWR - [220100193]SWR,KARNATAKA ,	04/1997	2,315.00 -	2,315.00	151.40	- -	12/2024	- -	0/0
464	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA ,	04/1996	1,382.78 1,382.78	1,382.78	7.35	03/2002 -	03/2024	264(O) -	0/0
465	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA ,	04/2011	1,801.01 1,801.01	1,801.01	57.70	- -	12/2023	- -	0/0
466	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA ,	04/2010	986.30 986.30	986.30	303.05	03/2016 -	12/2023	93(O) -	1/1
467	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA ,	04/2013	558.00 692.43	692.43	.00	- -	12/2023	- -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
468	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA ,	04/2011	832.47 832.47	832.47	.94	03/2016 -	03/2024	96(O) -	0/0
469	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA ,	04/2011	348.85 348.85	348.85	.36	- -	12/2023	- -	0/0
470	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA ,	04/2010	2,127.00 -	2,900.00	1,815.11	03/2023 -	03/2024	12(O) -	0/1
471	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA ,	04/2011	146.75 146.75	167.50	.34	- -	12/2023	- -	0/0
472	GADAG-WADI NL - [N22000299]SWR,KARNATAKA ,	04/2013	2,841.84 2,841.84	2,841.84	194.25	12/2018 -	12/2024	72(O) -	0/0
473	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA ,	04/2013	327.25 367.77	367.77	.00	- -	12/2023	- -	0/0
474	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA ,	04/2012	279.54 279.54	279.54	30.62	03/2016 -	12/2023	93(O) -	0/0
475	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA ,	03/2015	1,156.94 1,140.94	1,140.94	918.47	03/2020 -	03/2021	12(O) -	1/5
476	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA ,	03/2015	578.00 578.00	578.00	565.04	03/2020 -	03/2020	0(O) -	1/2
477	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA ,	03/1996	644.78 644.78	890.00	461.80	03/2017 -	03/2020	36(O) -	0/0
478	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA ,	10/1998	1,566.00 -	2,815.62	264.28	- -	-	-	0/0
479	KUMBALAM-TURAVUR - [N22000191]SR,KERALA ,	04/2011	252.96 -	252.96	8.50	- -	-	-	0/0
480	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA ,	04/2010	189.24 -	189.24	6.72	- -	-	-	0/0
481	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA ,	02/2015	1,431.90 -	1,431.90	75.00	- -	-	-	0/0
482	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA ,	02/2015	1,000.00 -	828.50	.08	- -	-	-	0/0
483	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA ,	02/2012	550.00 -	550.00	.00	03/2016 -	-	-	0/0
484	RAMGANJMUNDI-BHOPAL (NL) WCR - [220100314]WCR,MADHYA PRADESH ,	04/2001	424.60 -	2,909.99	1,975.34	03/2021 -	03/2023	24(O) -	0/14
485	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH ,	04/2005	383.79 1,473.76	1,413.76	1,351.73	- 01/2020	01/2020	- 0	0/0
486	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH ,	04/2008	3,503.69 3,975.22	3,975.22	1,801.98	03/2022 03/2023	03/2023	12(O) 0	0/0
487	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH ,	12/2015	1,763.93 -	1,762.94	867.52	03/2020 -	03/2023	36(O) -	1/1
488	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH ,	04/2011	1,485.85 -	1,485.85	1,196.74	12/2020 -	03/2021	3(O) -	0/0
489	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH ,	06/2016	2,478.23 -	2,478.23	477.93	03/2022 -	03/2023	12(O) -	0/10
490	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH ,	08/2016	582.13 -	1,247.64	228.36	03/2022 -	09/2022	6(O) -	1/1
491	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH ,	12/2015	174.00 -	174.00	164.41	03/2019 -	02/2020	11(O) -	0/0
492	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH ,	04/2010	585.93 1,268.32	1,268.32	687.95	02/2019 12/2020	12/2020	22(O) 0	0/1

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
493	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH ,	04/2015	1,370.00 1,370.94	1,370.94	332.76	12/2021 03/2023	03/2023	15(O) 4	0/0
494	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH ,	04/2016	700.00 603.69	603.69	146.09	06/2020 06/2021	06/2021	12(O) 0	0/0
495	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA ,	03/1996	495.44 1,781.98	2,980.41	1,457.78	03/2004 -	03/2021	204(O) -	0/0
496	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA ,	02/1997	2,271.50 -	4,517.49	2,495.07	03/2021 -	03/2022	12(O) -	0/0
497	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA ,	04/2008	5,300.00 -	918.53	284.75	03/2014 -	03/2021	84(O) -	0/0
498	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA ,	04/2012	714.10 -	714.10	65.20	04/2016 -	-	-	0/0
499	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA ,	04/2008	3,168.29 -	3,168.29	1,268.08	03/2023 -	03/2023	0(O) -	0/0
500	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA ,	04/2011	792.89 -	1,377.48	318.59	03/2021 -	03/2022	12(O) -	0/0
501	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA ,	04/2011	184.06 199.12	312.00	293.06	03/2019 03/2020	03/2020	12(O) 0	0/0
502	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA ,	04/2012	540.02 -	540.02	265.90	03/2022 -	03/2024	24(O) -	0/0
503	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA ,	02/2016	9,968.00 -	9,968.00	.00	03/2024 -	03/2024	0(O) -	0/0
504	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA ,	02/2016	2,425.00 -	5,341.68	.00	03/2024 -	03/2024	0(O) -	0/0
505	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA ,	02/2016	2,750.00 -	3,438.51	.00	03/2024 -	-	-	0/0
506	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA ,	02/2015	1,272.19 -	1,272.19	339.43	03/2022 -	03/2023	12(O) -	0/0
507	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA ,	02/2015	2,449.91 -	2,449.91	218.30	03/2023 -	03/2023	0(O) -	0/0
508	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA ,	02/2015	3,627.47 3,627.00	3,627.47	854.93	03/2024 -	03/2023	-12(O) -	0/0
509	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA ,	02/2016	1,876.00 -	2,081.27	230.40	03/2023 -	03/2023	0(O) -	0/0
510	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA ,	02/2016	1,035.16 -	1,035.16	138.46	03/2022 -	03/2024	24(O) -	0/0
511	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA ,	02/2016	637.95 -	637.95	76.12	03/2023 -	03/2024	12(O) -	0/0
512	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA ,	03/2009	713.48 -	2,300.00	2,131.56	03/2020 -	03/2021	12(O) -	0/0
513	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA ,	04/2015	723.78 -	723.78	.19	12/2025 -	03/2025	-9(O) -	0/0
514	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA ,	09/2016	1,908.51 2,686.63	2,686.63	540.55	03/2023 03/2023	03/2023	0(O) 0	0/1
515	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA ,	10/2013	305.00 -	305.00	261.83	03/2019 -	12/2019	-	0/0
516	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA ,	03/2010	265.88 -	265.88	.00	- -	-	-	0/0
517	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA ,	03/2012	217.38 -	217.38	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
518	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA ,	06/2018	229.00 852.50	852.50	39.69	12/2021 03/2023	03/2023	15(O) 0	0/1
519	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR ,	04/2003	4,454.17 13,809.00	12,524.00	9,599.02	03/2011 -	03/2022	132(O) -	0/0
520	NEW BG LINE FROM BYRNHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA ,	04/2010	906.46 -	6,000.60	263.12	03/2021 -	03/2021	0(O) -	0/0
521	BHAIRABI SAIRONG NL NEFR - [N22000100]NFR,MIZORAM ,	04/2008	2,393.47 4,968.00	5,021.45	3,183.01	03/2014 03/2022	03/2022	96(O) 0	0/0
522	GONDIA-JABALPUR(GC) (SECR) - [220100186]SECR,MULTI STATE ,	02/1997	511.86 1,756.00	1,756.00	1,679.29	04/2020 01/2021	01/2021	9(O) 0	0/1
523	NANGALDAM-TALWARA(NL) NR - [220100188]NR,MULTI STATE ,	03/1981	450.00 2,010.00	2,200.00	668.77	07/2012 -	03/2024	140(O) -	0/0
524	MUNEERABAD-MAHABOONAGAR(NL) SCR - [220100205]SCR,MULTI STATE ,	04/1997	1,723.00 1,780.29	3,472.59	970.69	03/2000 -	03/2021	252(O) -	0/0
525	LALITPUR-SATNA-REWA-SINGRULI NL (NCR) - [220100232]WCR,MULTI STATE ,	09/1998	247.66 -	8,248.50	1,986.78	05/2008 -	03/2023	178(O) -	0/9
526	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) NEFR - [220100266]NFR,MULTI STATE ,	04/2000	1,180.19 3,300.00	4,541.00	3,346.08	12/2008 -	03/2021	147(O) -	0/0
527	DEOGHAR - SULTANGANJ (INL) ER - [220100273]ER,MULTI STATE ,	04/2000	607.09 -	1,425.44	637.56	02/2013 -	03/2024	133(O) -	0/0
528	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE ,	04/2005	230.03 -	230.03	277.14	12/2022 -	12/2022	0(O) -	0/0
529	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE ,	03/2007	243.78 -	895.00	106.55	12/2021 -	12/2021	0(O) -	0/0
530	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE ,	03/2013	295.00 -	477.31	370.93	01/2019 -	01/2020	12(O) -	0/0
531	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE ,	04/2007	1,347.26 1,347.26	1,347.26	756.98	03/2022 03/2022	03/2022	0(O) 0	0/0
532	DAHOD-INDORE VIA SARDARPUR JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE ,	04/2007	1,640.04 1,640.04	1,640.04	756.11	03/2022 03/2023	03/2023	12(O) 0	0/0
533	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE ,	04/2011	2,082.75 -	4,262.36	185.90	- -	-	-	0/1
534	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE ,	04/2011	2,912.96 -	3,845.60	148.26	03/2022 -	12/2024	33(O) -	0/3
535	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE ,	04/2010	2,030.50 -	2,030.50	19.07	- -	-	-	0/0
536	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE ,	04/2010	651.00 -	1,009.00	7.96	03/2015 03/2025	03/2025	120(O) 0	0/0
537	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE ,	04/2008	415.67 -	549.75	15.55	- -	-	-	0/0
538	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE ,	04/2013	1,798.00 -	2,496.67	.04	03/2019 -	-	-	0/0
539	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE ,	04/2008	523.52 -	2,300.00	2.28	- -	-	-	0/0
540	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE ,	04/2007	270.14 -	457.08	373.51	- -	-	-	0/0
541	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE ,	04/2010	242.22 -	471.00	69.09	03/2020 -	03/2020	0(O) -	0/0
542	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE ,	04/2010	241.52 -	373.87	273.20	- -	06/2021	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
543	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE ,	04/2011	414.84 -	661.00	123.00	03/2020 -	03/2020	0(O) -	0/0
544	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE ,	04/1999	819.23 -	1,871.00	1,082.01	- -	-	-	0/0
545	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE ,	04/2011	120.70 -	1,800.00	187.92	03/2019 -	12/2019	-	0/0
546	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE ,	04/1987	406.99 -	545.70	148.49	03/2006 -	03/2025	228(O) -	0/0
547	SULTANGANJ-KATURIA VIA ASARGANJ TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE ,	04/2007	450.00 -	1,261.34	.00	- -	03/2025	- -	0/0
548	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE ,	04/2010	172.03 -	260.10	10.73	- -	03/2025	- -	0/0
549	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE ,	04/2013	915.98 -	2,137.81	300.18	03/2022 -	03/2025	36(O) -	0/0
550	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE ,	04/2011	288.35 -	402.48	402.48	- -	03/2020	- -	0/0
551	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE ,	04/2011	261.38 -	492.84	492.84	- -	05/2019	-	0/0
552	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE ,	04/2001	923.52 -	995.10	507.56	03/2016 -	03/2025	108(O) -	0/0
553	CHINPAI-SAINTHIA DOUBLING MM FOR PRANTI-SURI CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE ,	04/2005	595.51 -	769.40	103.08	03/2017 -	03/2025	96(O) -	0/0
554	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE ,	04/2010	174.56 -	174.56	71.42	- -	03/2025	- -	0/0
555	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE ,	04/2010	277.28 -	266.32	169.37	03/2016 -	03/2025	108(O) -	0/0
556	DANKUNI-CHANDANPUR 4TH LINE 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE ,	04/2010	365.17 -	296.43	275.76	03/2017 -	03/2025	96(O) -	0/0
557	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE ,	04/2010	157.94 -	157.94	51.75	11/2018 -	03/2021	28(O) -	0/0
558	BARIARPIUR-MANANPURVIA KHARAGPUER LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE ,	04/2007	450.55 -	250.55	20.12	- -	03/2025	- -	0/0
559	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE ,	04/2010	365.17 -	527.54	1.76	- -	03/2025	- -	0/0
560	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE ,	04/2011	542.18 -	693.80	474.79	03/2020 -	03/2021	12(O) -	0/0
561	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE ,	04/2011	175.80 -	260.83	260.83	- -	03/2021	- -	0/0
562	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE ,	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	108(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
563	NEW ALIPUR TO AKRA MM FOR BUDGE BUDGE-PUJALI NL PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE ,	04/2010	494.54 -	494.59	32.00	03/2005 -	03/2025	240(O) -	0/0
564	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE ,	04/2000	297.47 -	298.22	52.09	- -	03/2025	- -	0/0
565	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE ,	04/2003	337.96 -	336.96	70.20	- -	03/2025	- -	0/0
566	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE ,	04/2009	499.96 -	680.68	159.70	02/2012 -	03/2025	157(O) -	0/0
567	LILUAH-DANKUNI 3RD LINE MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE ,	04/2009	257.42 -	257.42	108.11	03/2014 -	03/2025	132(O) -	0/0
568	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE ,	04/2011	166.89 -	166.89	.02	- -	03/2025	- -	0/0
569	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE ,	04/2012	1,856.95 1,952.68	1,952.68	329.00	03/2023 -	03/2024	12(O) -	0/0
570	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE ,	04/2012	923.23 2,184.83	2,184.83	2.46	- -	-	-	1/1
571	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE ,	04/2007	336.91 -	791.39	517.05	- -	03/2022	- -	0/0
572	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE ,	04/2013	296.00 466.65	466.65	.00	- -	12/2023	- -	0/0
573	RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE ,	04/2007	2,062.30 2,062.30	2,062.30	932.12	- -	03/2025	- -	2/2
574	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE ,	04/2010	704.31 927.94	927.94	303.24	03/2020 03/2020	03/2020	0(O) 0	1/1
575	KADAPA-BANGALORE (NL) KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE ,	04/2008	2,132.77 2,132.77	2,132.77	350.17	03/2014 -	03/2024	120(O) -	1/1
576	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE ,	04/2012	250.93 -	310.70	287.10	- -	03/2024	- -	0/0
577	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE ,	05/2015	600.00 -	685.99	99.38	03/2020 -	04/2022	25(O) -	0/0
578	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE ,	05/2015	860.43 -	958.00	781.04	03/2020 -	03/2020	0(O) -	0/0
579	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE ,	03/2015	1,614.59 1,870.41	1,870.41	1,056.97	03/2019 -	03/2021	24(O) -	0/0
580	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE ,	05/2015	678.54 678.54	678.54	556.86	03/2019 -	02/2021	23(O) -	0/38
581	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE , Central Sector Projects	10/2006	11,589.00 30,357.00	28,181.00	.00	- -	-	-	0/0
582	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE ,	04/2015	2,063.03 2,063.03	2,063.03	880.17	03/2021 -	03/2023	24(O) -	0/0
583	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE ,	04/2015	636.38 -	636.38	.00	- -	-	-	0/0
584	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE ,	12/2015	1,08,000.00 -	1,08,000.00	6,708.69	12/2023 12/2023	12/2023	0(O) 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
585	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE ,	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	03/2020	0(O) -	0/0
586	CHANDIGARH-BADDI - [N22000467]NJR,MULTI STATE ,	04/2007	328.14 -	1,540.00	234.79	03/2023 -	03/2023	0(O) -	0/0
587	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NJR,MULTI STATE ,	03/2002	625.00 -	859.00	835.35	03/2016 -	03/2021	60(O) -	0/0
588	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND ,	04/2006	2,326.52 -	5,806.81	876.09	03/2015 -	10/2021	79(O) -	0/0
589	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND ,	04/2013	4,274.00 -	4,274.00	.00	03/2020 -	03/2020	0(O) -	0/0
590	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA ,	04/1994	2,923.13 3,791.66	3,791.66	1,270.24	03/2009 -	06/2024	183(O) -	0/0
591	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA ,	04/1996	1,185.64 -	1,844.47	1,883.44	12/2017 -	03/2020	27(O) -	0/0
592	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA ,	04/1998	1,202.70 -	1,202.70	1,008.33	02/2015 -	12/2021	82(O) -	0/0
593	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA ,	04/2000	133.41 207.00	396.00	388.21	03/2009 03/2009	06/2020	135(O) 0	1/1
594	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA ,	04/2005	810.78 198.07	1,928.07	780.24	06/2021 -	06/2024	36(O) -	0/0
595	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA ,	04/2010	149.90 -	230.00	54.46	03/2015 -	-	-	0/0
596	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA ,	03/2011	1,111.99 1,539.28	1,539.28	972.93	02/2019 03/2022	03/2022	37(O) 0	0/0
597	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA ,	03/2013	843.04 843.04	843.04	147.39	10/2020 03/2023	03/2023	29(O) 0	0/0
598	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA ,	03/2012	155.81 -	238.03	205.65	03/2020 -	03/2021	12(O) -	0/0
599	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA ,	04/2015	1,547.38 1,547.38	1,547.38	435.59	03/2022 03/2023	03/2023	12(O) 0	0/0
600	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA ,	04/2015	2,361.74 2,361.74	2,361.74	247.79	03/2022 -	03/2025	36(O) -	0/0
601	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA ,	04/2015	701.61 701.61	810.02	139.27	11/2018 -	03/2022	40(O) -	0/0
602	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA ,	04/2015	1,172.92 1,172.92	1,172.92	560.36	12/2018 03/2022	03/2023	51(O) 0	0/0
603	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA ,	11/2015	969.83 1,312.96	1,312.96	610.19	03/2020 03/2020	03/2021	12(O) 9	0/0
604	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA ,	01/1991	2,335.67 -	2,335.68	698.45	12/2024 -	12/2024	0(O) -	0/0
605	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA ,	03/2006	948.04 -	1,500.00	1,451.81	03/2020 -	03/2021	12(O) -	0/0
606	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA ,	03/2009	942.95 -	1,120.00	1,046.08	03/2019 -	06/2022	39(O) -	0/0
607	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA ,	04/2016	5,200.00 -	1,700.43	48.00	03/2020 -	06/2023	39(O) -	0/0
608	QADIAN-BEAS - [N22000295]NJR,PUNJAB ,	04/2011	205.22 -	841.90	1.73	- -	03/2024	- -	0/0
609	DAUSA-GANGAPUR CITY(NL) NWR - [220100184]NWR,RAJASTHAN ,	02/1997	410.08 780.98	886.41	568.73	02/2019 -	06/2021	28(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
610	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN ,	04/2012	246.08 -	348.55	248.71	12/2019 -	02/2021	14(O) -	0/0
611	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN ,	04/2013	236.93 -	350.45	232.02	10/2018 -	12/2019	-	0/0
612	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN ,	04/2013	822.00 -	1,099.54	.00	-	-	-	0/1
613	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN ,	04/2013	323.00 -	432.22	.00	-	-	-	0/0
614	MAVLI JUNCTION-BARI SADRI MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN ,	04/2013	420.18 -	420.18	199.53	03/2020 -	12/2020	9(O) -	0/0
615	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN ,	04/2011	213.39 -	303.56	285.01	11/2019 -	12/2020	13(O) -	0/0
616	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN ,	04/2013	242.09 281.03	410.00	381.92	02/2019 -	02/2020	12(O) -	0/0
617	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN ,	05/2015	873.71 -	1,980.21	4.60	-	-	-	0/0
618	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN ,	01/2011	493.17 -	493.17	443.19	03/2018 -	03/2020	24(O) -	0/0
619	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN ,	08/2018	808.85 -	808.85	81.26	08/2022 -	09/2022	1(O) -	0/0
620	SEVOK RANGPO NEFR - [N22000102]NFR,SIKKIM ,	04/2008	1,339.48 -	4,084.69	332.23	12/2015 -	-	-	0/0
621	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU ,	09/1995	303.98 -	980.00	683.11	03/2020 -	03/2021	12(O) -	0/0
622	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS MTP - [N22000028]MRTP,TAMIL NADU ,	04/2006	495.74 -	734.01	445.91	06/2013 -	-	-	1/4
623	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU ,	09/2007	724.69 -	2,072.50	1,471.60	02/2019 -	02/2020	12(O) -	0/0
624	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU ,	09/2006	227.40 -	900.00	63.28	-	-	-	0/0
625	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU ,	09/2006	582.83 -	2,300.00	243.44	-	-	-	0/0
626	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU ,	04/2008	151.84 -	1,105.00	3.34	02/2019 -	-	-	0/0
627	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU ,	04/2013	839.00 -	1,500.00	.62	-	-	-	0/0
628	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU ,	04/1999	198.68 -	556.64	305.22	-	-	-	0/0
629	ERODE-PALANI - [N22000199]SR,TAMIL NADU ,	04/2008	288.57 -	1,140.00	1.63	-	-	-	0/0
630	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU ,	04/2008	164.41 -	450.00	197.11	-	03/2020	-	0/0
631	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU ,	04/2007	931.98 -	951.24	753.41	-	03/2020	-	0/0
632	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU ,	10/2013	187.26 -	231.67	167.12	04/2014 -	03/2020	71(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
633	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU ,	02/1996	268.87 -	950.00	927.86	03/2005 -	-	-	0/0
634	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU ,	02/1999	257.00 257.00	257.00	268.31	03/2018 -	-	-	0/0
635	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU ,	02/2017	1,567.00 -	1,567.00	.00	03/2024 -	03/2026	24(O) -	0/0
636	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU ,	02/2015	1,700.00 -	1,003.00	252.02	03/2022 -	03/2022	0(O) -	0/0
637	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU ,	02/2015	760.00 -	1,182.31	446.00	03/2020 -	06/2021	15(O) -	0/0
638	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA ,	07/1998	458.25 458.25	458.26	3.83	- -	-	-	0/0
639	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA ,	04/2006	1,160.48 1,160.48	1,160.48	340.48	03/2010 -	03/2023	156(O) -	1/1
640	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA ,	04/2012	632.68 -	816.55	720.70	03/2016 -	12/2020	57(O) -	0/0
641	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA ,	04/2013	1,112.00 2,911.84	2,911.84	.92	- -	-	-	1/1
642	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES,TELANGANA ,	03/2015	636.38 -	636.38	392.54	03/2021 -	03/2021	0(O) -	3/3
643	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA ,	04/2015	773.94 -	773.94	556.16	12/2024 -	12/2024	0(O) -	0/0
644	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA ,	04/2017	119.73 176.17	449.39	298.13	03/2022 -	12/2022	9(O) -	0/0
645	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA ,	04/2012	569.63 670.00	670.00	82.81	03/2020 09/2021	09/2021	18(O) 0	2/3
646	ETAWAH-MAINPURI (NL) NCR - [220100318]NCR,UTTAR PRADESH ,	04/1997	120.00 -	346.00	345.51	12/2008 -	-	-	0/0
647	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH ,	02/2008	171.10 -	275.08	141.55	03/2012 -	-	-	0/0
648	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH ,	03/2013	307.00 -	1,409.09	.00	- -	-	-	0/0
649	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH ,	03/2013	643.00 -	644.00	.00	- -	-	-	0/0
650	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH ,	04/2012	1,229.00 -	1,230.00	103.72	-	03/2023	-	0/0
651	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH ,	04/2014	182.92 -	197.73	.00	- -	-	-	0/0
652	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH ,	03/2015	1,295.42 -	1,295.42	473.91	03/2022 -	12/2019	-	0/0
653	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR,UTTAR PRADESH ,	04/2015	668.70 668.00	680.00	330.00	03/2020 -	03/2020	0(O) -	4/6
654	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH ,	04/2015	943.60 -	750.56	485.98	03/2022 -	12/2024	33(O) -	0/0
655	LUCKNOW- PILIBHIT VIA SITAPUR LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH ,	04/2011	927.01 -	1,200.00	1,209.55	03/2019 -	03/2020	12(O) -	0/0
656	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH ,	04/2015	1,765.92 -	1,765.92	674.40	03/2023 -	12/2024	21(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
657	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH ,	03/2012	1,183.25 -	1,183.25	1,184.32	12/2020 -	12/2022	24(O) -	0/0
658	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH ,	08/2015	2,436.21 -	2,436.21	681.43	03/2020 -	03/2021	12(O) -	0/0
659	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH ,	08/2015	528.57 -	528.57	128.55	03/2019 -	03/2021	24(O) -	0/0
660	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH ,	04/2016	213.00 -	213.35	9.63	04/2016 -	06/2020	50(O) -	0/0
661	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH ,	04/2016	1,900.00 -	1,277.06	.00	01/2022 -	01/2022	0(O) -	0/0
662	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH ,	04/2017	150.00 -	150.00	.00	04/2017 -	10/2022	66(O) -	0/0
663	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH ,	04/2017	1,343.00 -	1,476.15	.00	01/2018 -	-	-	0/0
664	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH ,	04/2017	622.50 427.00	426.74	240.48	04/2017 -	01/2020	33(O) -	0/0
665	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH ,	04/2017	276.90 -	276.90	.00	04/2017 -	04/2022	60(O) -	0/0
666	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH ,	04/2016	602.50 -	714.34	34.88	-	-	-	0/0
667	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]NER,UTTAR PRADESH ,	04/2016	600.00 -	600.00	69.85	01/2022 -	01/2022	0(O) -	0/0
668	SHAHGANJ-BHATNI-PHEPHNA-INDARA MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH ,	04/2016	1,177.96 -	1,028.95	26.06	12/2019 -	04/2021	16(O) -	0/0
669	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH ,	03/2018	4,329.53 -	4,329.53	3.90	03/2023 -	03/2023	0(O) -	0/0
670	JHANSI BINA DOUBLING - [N22000496]NCR,UTTAR PRADESH ,	09/2016	2,001.00 -	2,001.00	416.59	03/2021 -	03/2021	0(O) -	0/6
671	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND ,	04/2003	142.45 -	228.40	.15	-	-	-	0/0
672	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND ,	04/2012	219.83 -	346.63	233.23	-	06/2020	-	0/0
673	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND ,	04/2011	16,216.00 -	16,216.00	1,941.37	12/2024 -	03/2025	3(O) -	0/0
674	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL) NEFR - [220100135]NFR,WEST BENGAL ,	04/1983	297.32 -	614.00	275.07	03/2019 -	03/2020	12(O) -	0/0
675	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL ,	04/1974	393.46 154.30	1,026.00	182.49	03/2007 03/2007	-	-	0/0
676	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL ,	03/2000	1,049.69 -	3,404.92	3,837.57	12/2006 -	-	-	0/0
677	TARAKESWAR - BISHNUPUR NEW BG LINE (NL) ER - [220100272]ER,WEST BENGAL ,	04/2000	1,188.91 -	1,619.48	872.43	03/2019 12/2009	03/2025	72(O) 0	0/0
678	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL ,	04/2007	1,106.62 -	1,091.59	877.32	12/2010 12/2017	03/2025	171(O) 0	7/7
679	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL,WEST BENGAL ,	04/2010	2,397.72 -	2,397.72	197.20	03/2016 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
680	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL ,	04/2010	2,298.42 -	2,733.86	40.13	03/2014 -	12/2025	141(O) -	0/0
681	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL ,	04/2010	3,951.98 -	4,724.30	2,307.00	03/2016 -	03/2025	108(O) -	0/0
682	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL ,	04/2010	2,913.51 -	4,639.00	871.04	03/2016 -	03/2025	108(O) -	0/0
683	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL ,	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	63(O) -	0/0
684	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL ,	04/2010	267.37 -	620.00	40.99	- 03/2025	03/2025	- 0	0/0
685	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL ,	04/2010	221.42 -	380.00	38.18	- 03/2022	03/2022	- 0	0/0
686	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL ,	04/2009	573.78 -	268.52	.03	- -	03/2025	- -	0/0
687	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL ,	04/2012	255.64 -	272.20	196.05	- -	09/2021	- -	0/0
688	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR, WEST BENGAL ,	04/2016	602.27 -	612.00	344.08	12/2021 -	03/2020	-21(O) -	0/0
689	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER, WEST BENGAL ,	04/1998	1,027.40 1,966.70	2,373.00	485.04	03/2003 03/2030	03/2030	324(O) 0	0/0
690	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]NFR, WEST BENGAL ,	02/1999	380.60 -	1,871.00	1,087.60	04/2010 -	-	-	0/0
	Total		4,59,394.75 -	6,71,692.95	2,06,153.91				33/139
	<u>HUMAN RESOURCE DEVELOPMENT</u>								
691	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM GOA. - [N42000002]CPWD, GOA ,	05/2019	303.90 -	303.90	.00	03/2020 -	03/2020	0(O) -	0/0
692	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]RITES, MEGHALAYA ,	09/2013	484.32 -	626.26	.00	09/2014 -	12/2020	75(O) -	0/0
693	STUDY IN INDIA - [N42000003]EDCIL, MULTI STATE ,	03/2018	150.00 -	150.00	.00	04/2018 -	-	-	0/0
694	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION - [N42000004]IITKGP, MULTI STATE ,	08/2018	418.00 -	418.00	110.00	03/2019 -	-	-	0/0
	Total		1,356.22 -	1,498.16	110.00				0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
695	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS ,	03/2015	262.97 -	262.97	.00	10/2018 -	-	-	0/4
696	2 LANE WITH HARD SHOLDER REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS ,	03/2017	409.85 -	409.85	21.11	12/2017 -	-	-	0/4
697	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS ,	03/2015	277.17 -	277.17	159.49	04/2017 -	-	-	3/4
698	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS ,	02/2018	391.00 -	391.00	22.17	10/2018 -	-	-	0/4
699	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS ,	03/2018	234.27 -	234.27	11.03	10/2018 -	-	-	1/4
700	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MoRTH,A & N ISLANDS ,	11/2017	237.80 -	238.00	7.48	11/2019 -	-	-	0/0
701	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH,A & N ISLANDS ,	11/2017	257.34 -	238.00	41.09	11/2019 -	-	-	0/0
702	AJANTHA TO BULDHANA - [N24001008]MoRTH,A & N ISLANDS ,	02/2017	401.00 401.00	401.00	121.81	07/2019 -	07/2019	-	0/4
703	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH , PPP (BOT)	04/2011	571.00 -	571.00	582.53	10/2013 -	-	-	0/0
704	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2011	1,535.00 -	1,535.00	3,260.65	05/2014 12/2019	03/2020	70(O) 3	0/0
705	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]MoRTH,ANDHRA PRADESH ,	07/2015	333.21 333.21	333.21	256.11	12/2015 -	-	-	0/2
706	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]MoRTH,ANDHRA PRADESH , EPC	01/2014	195.45 -	195.45	.00	11/2014 -	-	-	0/4
707	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]MoRTH,ANDHRA PRADESH , EPC	03/2015	271.45 -	271.45	182.45	10/2015 01/2020	01/2020	51(O) 27	3/4
708	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]MoRTH,ANDHRA PRADESH ,	07/2015	333.21 -	333.21	256.11	12/2015 -	-	-	0/2
709	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]MoRTH,ANDHRA PRADESH , EPC	10/2015	333.21 -	353.89	256.11	11/2015 -	-	-	0/0
710	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH ,	01/2016	1,134.97 -	1,134.97	806.94	11/2018 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
711	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH ,	09/2014	1,684.00 -	1,684.00	54.13	02/2017 -	-	-	0/0
712	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]NHAI,ANDHRA PRADESH ,	03/2017	648.32 -	511.94	511.34	03/2020 -	03/2020	0(O) -	0/0
713	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH ,	03/2017	1,041.62 -	1,187.10	829.16	03/2020 -	05/2020	2(O) -	0/0
714	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH , Central Sector Projects	06/2017	648.33 -	306.00	157.33	06/2017 -	08/2020	38(O) -	0/0
715	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH ,	12/2017	328.67 -	328.67	206.07	- -	-	-	0/0
716	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH ,	12/2017	1,323.15 -	1,323.15	403.93	- -	07/2021	- -	0/0
717	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH ,	12/2017	357.00 -	357.00	70.71	- -	-	-	0/0
718	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH ,	02/2018	1,959.00 -	1,959.00	706.39	- -	07/2021	- -	0/0
719	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH ,	03/2018	1,532.62 2,499.00	2,499.00	730.93	03/2021 -	04/2021	1(O) -	2/4
720	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH ,	03/2018	1,550.98 1,730.07	1,550.98	786.78	- -	07/2021	- -	0/0
721	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH ,	03/2018	565.09 -	565.09	191.77	- -	02/2021	- -	0/0
722	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH ,	03/2018	314.43 -	314.43	46.12	- -	12/2020	- -	0/0
723	CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH ,	03/2018	557.30 -	557.30	211.24	- 06/2020	06/2020	- 3	0/0
724	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]MoRTH,ANDHRA PRADESH ,	10/2015	333.21 -	355.89	294.81	12/2015 01/2020	01/2020	49(O) 37	2/3
725	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929]MoRTH,ANDHRA PRADESH ,	09/2016	372.68 -	372.68	185.04	02/2017 12/2019	02/2019	-	2/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
726	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO - [N24000930]MoRTH,ANDHRA PRADESH ,	11/2016	378.24 -	378.24	307.17	01/2018 01/2020	01/2020	24(O) 0	4/4
727	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931]MoRTH,ANDHRA PRADESH ,	11/2016	290.15 -	290.15	73.11	05/2017 03/2020	03/2020	34(O) 10	1/4
728	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932]MoRTH,ANDHRA PRADESH ,	01/2017	319.28 -	319.28	111.98	08/2017 03/2020	03/2020	31(O) 7	1/4
729	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]MoRTH,ANDHRA PRADESH ,	02/2017	429.43 -	429.43	255.68	11/2017 03/2020	03/2020	28(O) 4	3/4
730	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934]MoRTH,ANDHRA PRADESH ,	03/2018	228.32 -	228.32	48.15	08/2018 03/2020	03/2020	19(O) 0	2/4
731	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU - [N24000936]MoRTH,ANDHRA PRADESH ,	03/2018	244.95 245.00	244.95	136.22	08/2018 02/2020	02/2020	18(O) 0	2/3
732	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]MoRTH,ANDHRA PRADESH ,	03/2018	289.67 290.00	289.67	105.02	08/2018 02/2020	02/2020	18(O) 0	2/4
733	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938]MoRTH,ANDHRA PRADESH ,	03/2018	297.12 294.00	294.12	373.98	07/2018 01/2020	01/2020	18(O) 0	4/4
734	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]MoRTH,ANDHRA PRADESH ,	03/2018	504.19 504.00	504.19	248.37	11/2018 05/2020	05/2020	18(O) 0	2/4
735	REHABILITATION AND UPGRADATION OF KARNATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]MoRTH,ANDHRA PRADESH ,	03/2016	995.09 995.00	995.09	419.22	05/2016 07/2020	07/2020	50(O) 26	2/4
736	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963]MoRTH,ANDHRA PRADESH ,	01/2018	418.03 -	418.03	194.62	08/2018 08/2020	08/2020	24(O) 0	2/4
737	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964]MoRTH,ANDHRA PRADESH ,	08/2016	350.61 -	350.61	310.25	01/2017 04/2020	04/2020	39(O) 21	3/4
738	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]MoRTH,ANDHRA PRADESH ,	01/2016	386.09 -	386.09	184.26	05/2016 12/2019	05/2018	-	2/4
739	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966]MoRTH,ANDHRA PRADESH ,	01/2016	348.95 -	348.95	169.46	08/2016 03/2020	03/2020	43(O) 19	2/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
740	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967]MoRTH,ANDHRA PRADESH ,	03/2016	444.84 -	444.84	273.88	09/2016 03/2020	03/2020	42(O) 18	3/4
741	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]MoRTH,ANDHRA PRADESH ,	11/2016	376.25 -	376.25	228.69	08/2017 02/2020	02/2020	30(O) 6	2/4
742	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969]MoRTH,ANDHRA PRADESH ,	01/2017	263.45 -	263.45	60.26	09/2017 12/2020	12/2020	39(O) 15	0/4
743	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]MoRTH,ANDHRA PRADESH ,	01/2017	576.48 -	576.48	237.30	01/2018 12/2020	01/2020	24(O) 0	1/4
744	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S - [N24001183]MoRTH,ANDHRA PRADESH ,	07/2014	251.55 -	251.55	7.74	02/2015 -	-	-	0/0
745	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]MoRTH,ARUNACHAL PRADESH , ITEM RATE	12/2011	156.63 276.00	276.00	147.65	02/2012 -	-	-	0/0
746	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]MoRTH,ARUNACHAL PRADESH , ITEM RATE	11/2010	305.49 -	305.49	131.08	03/2011 -	-	-	0/0
747	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]MoRTH,ARUNACHAL PRADESH , ITEM RATE	03/2012	207.03 389.45	389.45	308.09	05/2012 05/2015	12/2019	-	0/0
748	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	194.11 -	194.11	181.03	05/2018 -	08/2019	-	4/4
749	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL,ARUNACHAL PRADESH , EPC	10/2015	179.82 -	179.82	197.77	01/2019 -	-	-	4/4
750	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH , EPC	07/2015	197.16 197.16	197.16	81.53	10/2018 09/2015	09/2018	-	1/4
751	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	394.00 -	394.00	325.08	06/2018 -	03/2020	21(O) -	2/3
752	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450 TO KM 605.600(EXISTING CHAINAGE FROM KM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH ,	01/2016	183.65 -	183.65	129.11	11/2016 -	-	-	3/4
753	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH ,	04/2016	245.79 -	245.79	129.43	- -	09/2020	- -	2/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
754	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH ,	04/2016	198.00 -	198.00	184.62	10/2016 -	10/2019	-	3/4
755	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH ,	11/2015	434.06 -	434.06	172.89	- -	12/2020	- -	2/4
756	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH ,	12/2016	138.93 155.00	155.00	79.91	01/2017 -	01/2020	36(O) -	2/4
757	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH ,	01/2017	1,253.10 -	1,253.10	204.77	03/2017 -	03/2022	60(O) -	1/4
758	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH ,	03/2017	284.09 284.09	284.09	96.13	04/2017 03/2018	03/2021	47(O) 0	1/4
759	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH ,	02/2017	195.23 -	195.23	62.01	04/2017 -	-	-	1/4
760	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH ,	02/2017	203.36 -	203.36	72.88	04/2017 -	-	-	1/4
761	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH ,	01/2017	194.66 -	194.66	84.11	04/2017 -	-	-	2/4
762	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH ,	02/2017	168.32 168.32	168.32	40.78	04/2017 02/2018	02/2021	46(O) 0	1/4
763	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH ,	02/2017	180.57 180.57	180.57	16.80	04/2017 02/2018	02/2021	46(O) 0	0/4
764	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH ,	02/2017	216.71 216.71	216.71	25.17	04/2017 02/2018	02/2021	46(O) 0	0/4
765	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH ,	02/2017	167.28 167.28	167.28	21.54	04/2017 02/2018	02/2021	46(O) 0	1/1
766	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH ,	01/2017	198.22 -	198.22	84.11	04/2017 -	-	-	2/4
767	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH ,	03/2018	392.60 -	392.60	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
768	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH ,	12/2016	200.44 -	200.44	79.80	- -	-	-	0/0
769	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH ,	03/2017	1,718.59 -	1,718.59	204.77	- -	-	-	0/0
770	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 37.500 TO KM - [N24000947]NHIDCL,ARUNACHAL PRADESH ,	05/2016	259.52 -	259.52	184.51	- -	-	-	0/0
771	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH ,	09/2016	568.92 -	568.92	172.88	- -	-	-	0/0
772	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH ,	12/2016	188.78 -	188.78	59.98	- -	-	-	0/0
773	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH ,	02/2017	175.06 175.06	175.06	29.08	- 04/2019	04/2022	- 0	0/0
774	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL,ARUNACHAL PRADESH ,	02/2017	176.12 176.12	176.12	28.16	- 04/2019	04/2022	- 0	0/0
775	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D - [N24000974]NHIDCL,ARUNACHAL PRADESH ,	02/2017	199.02 199.02	199.02	13.82	- 02/2018	02/2021	- 0	0/0
776	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D - [N24000975]NHIDCL,ARUNACHAL PRADESH ,	02/2017	184.88 184.88	184.88	7.68	- 02/2018	02/2021	- 0	0/0
777	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL,ARUNACHAL PRADESH ,	10/2015	210.50 210.50	210.50	122.09	- 01/2016	01/2019	-	0/0
778	BORDUMSA NAMCHIK (BURIDEHING - JAIRAMPUR) ROAD ON NH-52B (NEW NH-215) FROM KM. 0.15 (STARTING CHAIN - [N24000977]NHIDCL,ARUNACHAL PRADESH ,	07/2015	189.91 -	189.91	154.43	- -	-	-	4/4
779	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN - [N24000978]NHIDCL,ARUNACHAL PRADESH ,	03/2015	172.75 -	172.75	120.18	- -	-	-	3/4
780	TWO-LANING OF HAYULIANG– HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI - [N24000979]NHIDCL,ARUNACHAL PRADESH ,	01/2017	256.66 -	256.66	24.14	- -	-	-	1/4
781	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH,ARUNACHAL PRADESH ,	09/2011	1,979.00 -	1,979.00	1,189.58	- 03/2020	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
782	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH,ARUNACHAL PRADESH ,	11/2016	243.89 -	243.89	128.46	- -	09/2020	- -	0/0
783	HARANGAJO TO MAIBANG (AS-23) KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM ,	12/2003	280.00 520.00	520.00	492.41	02/2009 07/2019	07/2019	-	0/0
784	MAIBANG TO LUMDING (AS-25) KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM ,	12/2003	199.81 340.14	340.14	319.96	04/2009 03/2011	08/2019	-	0/0
785	MAIBANG TO LUMDING (AS-26) KM.60.500 TO KM.83.400 NH-54 - [240106279]NHAI,ASSAM ,	12/2003	167.64 435.78	435.78	427.96	11/2008 07/2011	01/2014	-	0/0
786	MAIBANG TO LUMDING (AS-24) KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM ,	12/2003	155.04 255.23	255.23	251.39	11/2008 01/2011	08/2013	-	0/0
787	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM ,	12/2003	245.00 -	174.34	225.65	03/2008 -	08/2020	149(O) -	0/0
788	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM ,	12/2003	225.00 -	225.00	328.47	06/2008 -	09/2019	-	0/0
789	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM ,	12/2003	208.00 -	230.00	340.21	04/2008 -	03/2020	143(O) -	0/0
790	DHARAMTUL TO SONAPUR KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM ,	12/2003	160.00 -	167.98	223.81	05/2008 -	06/2019	-	0/0
791	HARANGAJO TO MAIBANG NH-54 - [N24000062]NHAI,ASSAM ,	12/2003	196.00 655.17	655.17	655.17	07/2009 10/2018	10/2018	-	0/0
792	BRAHMPUTRA BRIDGE NH NO-31 - [N24000063]NHAI,ASSAM ,	12/2003	217.61 -	360.84	454.21	04/2010 -	07/2019	-	0/0
793	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM , EPC	05/2015	454.89 -	454.89	141.83	05/2018 05/2020	12/2020	31(O) 0	2/4
794	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM , EPC	06/2015	437.39 -	437.39	10.01	06/2018 12/2020	12/2021	42(O) 0	0/4
795	FOUR LANING OF JHANJI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM , EPC	06/2015	463.49 -	463.49	26.15	06/2018 01/2021	12/2021	42(O) 0	0/4
796	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL,ASSAM , EPC	06/2016	829.00 -	829.00	311.84	01/2019 -	-	-	2/4
797	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM , EPC	03/2015	168.39 -	168.39	84.69	11/2018 -	-	-	4/4
798	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM , EPC	10/2014	588.95 -	588.95	403.00	11/2018 -	-	-	2/4
799	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]MoRTH,ASSAM , EPC	11/2010	268.08 -	268.08	203.15	05/2017 -	-	-	0/0
800	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]MoRTH,ASSAM , ITEM RATE	11/2010	470.20 -	630.36	386.98	02/2011 -	-	-	0/0
801	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]MoRTH,ASSAM , EPC	11/2014	218.31 -	307.47	263.85	02/2018 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
802	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37 ON EPC BASIS - [N24000429]NHIDCL, ASSAM , EPC	12/2015	225.02 -	159.20	26.00	12/2018 -	-	-	1/4
803	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL, ASSAM , EPC	12/2015	223.30 -	223.30	84.69	06/2018 -	-	-	3/4
804	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL, ASSAM , EPC	01/1991	520.01 -	520.01	56.63	-	-	-	1/4
805	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL, ASSAM , EPC	12/2015	289.99 -	289.99	15.37	12/2018 -	-	-	0/4
806	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL, ASSAM , EPC	01/2016	294.17 -	294.17	76.25	01/2016 02/2019	04/2021	63(O) 0	1/4
807	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL, ASSAM , EPC	01/2016	252.00 -	252.00	11.04	01/2016 12/2021	-	-	0/4
808	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL, ASSAM ,	03/2015	829.00 -	829.00	311.86	01/2016 -	-	-	2/3
809	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL, ASSAM ,	10/2017	818.00 -	818.00	63.08	-	06/2020	-	0/4
810	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0 KM 54/0 TO KM 61/0 KM 69/0 TO KM 80/0 AN - [N24001152]MoRTH, ASSAM ,	09/2018	160.00 -	160.00	.50	09/2021 -	09/2021	0(O) -	0/0
811	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM - [N24001153]MoRTH, ASSAM ,	11/2010	197.37 -	197.37	88.86	02/2014 -	12/2019	-	0/0
812	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL, ASSAM ,	03/2017	1,049.51 -	1,049.51	89.16	-	-	-	0/0
813	PATNA-MUZZAFFARPUR - [N24000165]NHAI, BIHAR , PPP (ANNUITY)	08/2010	671.30 -	671.30	1,132.48	02/2013 -	03/2020	85(O) -	3/4
814	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, BIHAR , PPP (BOT)	09/2011	574.00 -	574.00	768.73	03/2014 -	-	-	0/0
815	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, BIHAR ,	10/2011	375.09 -	375.09	494.33	04/2014 -	-	-	0/0
816	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, BIHAR , PPP (ANNUITY)	01/2011	575.00 -	575.00	850.24	07/2013 -	03/2020	80(O) -	2/3
817	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI, BIHAR , PPP (ANNUITY)	05/2011	511.54 585.00	591.00	571.86	11/2013 12/2019	03/2020	76(O) 0	0/0
818	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH, BIHAR , EPC	01/1991	675.00 -	675.00	154.56	-	-	-	0/0
819	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MoRTH, BIHAR , ITEM RATE	01/1991	282.41 -	322.01	278.45	08/2016 -	-	-	0/0
820	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MoRTH, BIHAR , ITEM RATE	01/1991	358.22 -	377.64	325.19	10/2016 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
821	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR ,	08/2015	556.07 -	556.07	.00	- -	-	-	0/0
822	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR ,	12/2015	1,041.10 -	1,041.10	214.34	04/2019 -	-	-	0/0
823	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR ,	08/2015	814.04 -	825.17	646.72	- -	01/2020	-	2/3
824	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR ,	08/2015	322.09 -	322.09	77.53	04/2018 -	12/2020	32(O) -	0/0
825	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR ,	01/1991	642.41 -	681.67	402.94	- -	10/2020	-	1/2
826	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR ,	12/2015	1,167.45 -	1,167.45	113.26	- -	12/2019	-	0/0
827	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR ,	08/2015	399.54 -	297.27	509.75	04/2019 -	-	-	3/4
828	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MoRTH,BIHAR ,	01/1991	478.35 -	478.35	.00	- -	-	-	0/0
829	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR ,	08/2015	854.80 -	854.80	558.04	- -	-	-	3/4
830	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR ,	08/2015	516.13 -	516.13	395.25	04/2018 -	-	-	4/4
831	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]MoRTH,BIHAR , EPC	01/1991	154.62 -	154.62	.00	- -	-	-	0/0
832	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]MoRTH,BIHAR , EPC	01/1991	319.68 -	369.77	113.67	- -	-	-	0/0
833	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MoRTH,BIHAR ,	10/2013	278.39 -	278.39	.00	08/2014 -	-	-	0/0
834	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MoRTH,BIHAR ,	11/2013	683.83 -	560.70	597.00	07/2016 -	-	-	0/0
835	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MoRTH,BIHAR ,	02/2014	665.50 -	665.50	.00	07/2016 -	-	-	0/0
836	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MoRTH,BIHAR ,	02/2016	178.85 -	152.62	40.44	05/2016 -	-	-	0/0
837	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MoRTH,BIHAR ,	02/2016	369.77 -	369.77	.00	06/2016 -	-	-	0/0
838	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MoRTH,BIHAR ,	02/2016	553.30 -	478.35	289.14	05/2016 -	-	-	0/0
839	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH,BIHAR ,	01/2014	1,408.85 -	925.87	586.18	10/2016 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
840	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPR - [N24000580]MoRTH,BIHAR ,	03/2015	206.80 -	206.80	74.04	07/2016 -	-	-	0/0
841	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MoRTH,BIHAR ,	08/2015	288.24 -	288.24	286.46	11/2015 -	-	-	0/0
842	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI,BIHAR ,	05/2015	581.84 -	581.84	89.69	05/2017 -	04/2019	-	0/0
843	REHABILITATION OF 4-LANE 5.575 KM LONG 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH,BIHAR ,	08/2016	1,742.01 -	1,742.01	1,034.37	12/2016 -	-	-	0/0
844	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR ,	03/2017	672.89 -	736.01	.00	03/2020 -	03/2020	0(O) -	0/0
845	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR ,	03/2017	235.48 -	227.77	11.00	03/2020 -	05/2021	14(O) -	0/0
846	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR , Central Sector Projects	08/2017	950.64 -	950.64	102.51	08/2017 -	02/2022	54(O) -	0/0
847	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR ,	12/2017	2,598.00 -	2,598.00	.00	- -	-	-	0/0
848	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR ,	01/2018	573.70 -	573.70	.00	- -	-	-	0/0
849	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR ,	01/2018	895.39 -	895.39	.00	- -	-	-	0/0
850	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR ,	03/2018	496.20 -	496.20	.00	- -	-	-	0/0
851	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR ,	09/2018	1,478.40 -	1,478.40	.00	- -	-	-	0/0
852	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C - [N24000999]MoRTH,BIHAR ,	11/2016	230.34 -	230.34	178.39	10/2019 -	-	-	0/0
853	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH,BIHAR ,	03/2018	153.24 -	153.24	2.06	- -	-	-	0/0
854	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]MoRTH,BIHAR ,	05/2014	199.98 -	199.98	153.43	08/2016 -	12/2020	52(O) -	0/0
855	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR ,	02/2019	2,926.42 -	2,926.42	.00	- -	-	-	0/0
856	WIDENING OF SL TO 2 L KM. 107-184.80 SUKUMA TO KONTA ON NH 221 - [N24001223]MoRTH,CHANDIGARH ,	03/2010	179.89 271.00	271.00	.00	03/2013 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
857	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1 - [N24001225]MoRTH,CHHATISGARH ,	12/2010	169.26 299.00	299.00	.00	01/2019 -	-	-	0/0
858	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]MoRTH,CHHATISGARH , EPC	12/2015	291.05 -	291.05	182.16	- -	-	-	0/0
859	REHABILITATION AND UPGRADE OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]MoRTH,CHHATISGARH , EPC	11/2015	485.44 -	485.44	447.13	12/2015 -	-	-	0/0
860	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH ,	12/2015	596.67 -	596.67	405.42	05/2018 10/2019	10/2019	-	0/0
861	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH ,	12/2015	509.13 -	509.13	412.66	04/2018 08/2018	08/2018	-	0/0
862	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH ,	12/2015	726.67 598.13	598.13	414.73	04/2018 03/2020	03/2020	23(O) 0	0/0
863	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH ,	03/2018	1,029.96 -	1,261.05	97.55	- 03/2021	03/2021	- 0	0/0
864	REHABILITATION AND UPGRADE OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]MoRTH,CHHATISGARH ,	01/2016	497.14 -	497.14	187.31	08/2016 -	-	-	0/0
865	REHABILITATION AND UPGRADE OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218]MoRTH,CHHATISGARH ,	11/2015	335.32 -	335.32	214.60	06/2017 -	-	-	0/0
866	REHABILITATION AND UPGRADE OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]MoRTH,CHHATISGARH ,	01/2016	476.20 544.00	544.00	372.74	09/2016 -	-	-	0/0
867	REHABILITATION AND UPGRADE OF NH 200 FROM KM 127.500 TO 178.944 DARRIGHAT TO BANARI SECTION - [N24001220]MoRTH,CHHATISGARH ,	03/2016	491.52 -	491.52	473.67	09/2016 -	-	-	0/0
868	REHABILITATION AND UPGRADE OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]MoRTH,CHHATISGARH ,	01/2016	624.98 -	624.98	253.27	10/2016 -	-	-	0/0
869	REHABILITATION AND UPGRADE OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222]MoRTH,CHHATISGARH ,	03/2016	452.94 -	452.94	66.25	07/2016 -	-	-	0/0
870	REHABILITATION AND UPGRADE OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO - [N24001224]MoRTH,CHHATISGARH ,	03/2017	423.79 -	423.79	158.78	01/2018 -	-	-	0/0
871	REHABILITATION AND UPGRADE OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226]MoRTH,CHHATISGARH ,	12/2014	496.02 -	496.02	225.69	03/2015 -	-	-	0/0
872	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228]MoRTH,CHHATISGARH ,	11/2017	188.80 -	188.80	.00	05/2019 -	-	-	0/0
873	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 - [N24001229]MoRTH,CHHATISGARH ,	12/2014	379.16 -	379.16	.00	11/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
874	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8 - [N24001184]NHIDCL,DELHI ,	07/2017	269.69 -	269.69	.00	09/2019 -	-	-	0/0
875	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDEAPAR BRIDGE - [N24000251]MoRTH,GOA , EPC	03/2015	297.00 -	297.00	290.64	04/2018 -	-	-	0/1
876	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]MoRTH,GOA ,	03/2015	298.33 -	298.33	160.33	- -	-	-	0/4
877	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]MoRTH,GOA , EPC	03/2015	184.05 -	184.05	96.58	- -	-	-	2/4
878	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]MoRTH,GOA , EPC	03/2015	280.16 -	290.59	219.47	- -	-	-	3/4
879	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH,GOA , EPC	10/2015	936.40 -	936.40	262.25	- -	-	-	0/0
880	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH,GOA , EPC	12/2015	773.98 -	773.98	259.66	- -	-	-	0/0
881	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MoRTH,GOA , EPC	12/2015	819.95 -	819.95	193.63	- -	-	-	0/0
882	PATRADEVI TO KARASWADA 4L - [N24001004]MoRTH,GOA ,	03/2017	634.32 634.32	634.32	109.33	05/2020 -	05/2020	0(O) -	1/4
883	KARASWADA TO BAMBOLIM - [N24001005]MoRTH,GOA ,	03/2017	852.67 852.67	852.67	86.04	12/2019 -	12/2019	-	1/4
884	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT , PPP (BOT)	03/2010	1,509.10 3,787.21	1,509.10	3,684.44	09/2012 12/2019	-	-	2/3
885	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT , PPP (BOT)	01/2011	953.88 -	953.88	976.79	07/2013 11/2020	11/2020	88(O) 0	0/0
886	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT , PPP (BOT)	01/2013	2,125.24 2,125.24	2,125.24	4,669.71	12/2015 -	-	-	3/3
887	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT ,	03/2014	503.16 -	503.16	389.50	08/2016 -	10/2017	-	0/0
888	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT ,	05/2016	998.18 -	998.18	441.80	- -	-	-	2/2
889	FOUR LANING OF TALAJA – MAHUA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT ,	05/2016	834.64 -	834.64	319.33	- -	-	-	1/1
890	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT ,	05/2016	723.64 -	723.64	313.19	- -	-	-	2/2
891	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT ,	05/2016	763.08 -	763.08	391.13	- -	-	-	2/2
892	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT ,	05/2016	425.60 241.41	425.60	105.83	- -	-	-	0/0
893	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT ,	05/2016	364.56 -	392.00	286.99	- -	08/2020	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
894	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT ,	07/2016	829.97 -	829.97	194.67	- -	01/2020	- -	0/0
895	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT ,	12/2016	417.19 -	417.19	264.05	- -	09/2019	-	0/3
896	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT ,	01/2017	1,251.11 -	1,251.11	1,084.26	- -	01/2021	- -	0/0
897	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT ,	06/2017	1,958.88 1,993.81	1,993.81	1,116.85	06/2020 02/2018	02/2021	8(O) 0	0/3
898	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT , Central Sector Projects	10/2017	232.49 -	232.49	.00	10/2017 -	11/2019	-	0/0
899	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT ,	02/2018	1,052.21 1,449.00	1,449.00	342.39	- -	01/2021	- -	0/0
900	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT ,	03/2018	2,702.05 -	2,043.00	.00	- 05/2018	01/2021	- 0	0/0
901	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT ,	03/2018	1,437.64 1,687.00	1,437.64	564.11	- 12/2018	07/2021	- 0	0/0
902	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT ,	03/2018	1,161.39 1,404.00	1,161.39	.00	- 11/2021	-	-	0/0
903	WIDENING FROM TWO LANE TO FOUR LANE WITH PAVED SHOULDER AND STRENGTHNING OF EXISTING PAVEMENT BETWEE - [N24000920]MoRTH,GUJARAT ,	03/2016	223.67 -	223.67	112.81	02/2017 -	-	-	4/4
904	UPGRADATION TO 2 LANE WITH PAVED SHOULDER WITH RIGID PAVEMENTS FROM 37/400 TO KM 66/700 ON NH 848 ON - [N24000921]MoRTH,GUJARAT , EPC	03/2016	208.34 -	208.34	112.87	02/2016 -	-	-	0/4
905	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922]MoRTH,GUJARAT , EPC	12/2017	867.97 -	867.97	232.58	11/2018 -	-	-	1/4
906	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEEN - [N24000923]MoRTH,GUJARAT , EPC	03/2018	464.07 -	464.07	166.81	11/2018 -	-	-	2/4
907	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]MoRTH,GUJARAT , EPC	10/2018	400.76 -	400.76	64.52	05/2019 -	-	-	1/4
908	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926]MoRTH,GUJARAT , EPC	08/2017	962.43 -	962.43	115.08	03/2018 -	-	-	0/4
909	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197]MoRTH,GUJARAT ,	03/2018	351.00 -	351.00	.49	06/2021 -	06/2021	0(O) -	0/0
910	DELHI HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA , PPP (BOT)	04/2007	486.00 -	486.00	470.01	05/2010 -	03/2020	118(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
911	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA , PPP (BOT)	05/2009	1,108.00 2,967.50	2,967.50	3,990.72	11/2011 -	03/2020	100(O) -	0/0
912	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA ,	08/2015	723.54 1,286.84	1,286.84	1,163.65	02/2018 10/2017	-	-	0/0
913	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA ,	12/2015	602.95 507.70	507.70	496.22	06/2016 -	12/2019	-	0/0
914	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA ,	01/2016	574.28 537.16	537.16	514.61	07/2018 -	11/2019	-	0/0
915	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA , PPP (BOT)	07/2015	2,128.72 -	2,128.72	971.24	04/2019 -	-	-	0/0
916	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA ,	11/2015	867.66 1,464.24	1,464.24	1,255.55	05/2018 02/2018	-	-	0/0
917	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA ,	08/2016	248.97 -	248.97	249.15	05/2019 -	03/2020	10(O) -	0/0
918	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA ,	09/2016	1,004.67 -	813.45	577.21	05/2019 -	02/2019	-	0/0
919	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA ,	03/2017	639.79 -	552.90	578.15	03/2020 -	03/2020	0(O) -	0/0
920	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA ,	03/2018	1,484.30 -	1,484.30	133.06	- -	12/2020	- -	0/0
921	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA ,	03/2018	275.12 -	275.12	134.80	- -	03/2020	- -	0/0
922	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTI - [N24000837]NHAI,HARYANA ,	03/2018	307.79 -	307.79	160.12	- -	03/2020	- -	0/0
923	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA ,	03/2018	634.70 931.21	931.21	143.54	- -	07/2021	- -	0/0
924	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA ,	03/2018	795.50 -	799.30	128.56	- -	07/2021	- -	0/0
925	REHABILITATION AND UPGADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA ,	03/2018	198.05 -	198.05	103.34	- -	03/2020	- -	0/0
926	REHABILITATION AND UPGADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA ,	03/2018	181.78 -	181.78	76.56	- -	06/2020	- -	0/0
927	REDESIGNING REHABILITATION AND UPGADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA ,	03/2018	551.58 -	551.58	305.46	- -	03/2020	- -	0/0
928	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]MoRTH,HARYANA ,	01/2017	247.25 -	247.25	144.71	03/2019 06/2020	06/2020	15(O) 9	0/0
929	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) - [N24000908]MoRTH,HARYANA ,	01/2017	276.01 -	276.01	187.39	03/2019 07/2019	-	-	0/0
930	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI,HARYANA ,	01/2019	1,051.91 -	1,051.91	301.49	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
931	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI,HARYANA ,	01/2019	1,120.06 -	1,120.06	250.18	- -	-	-	0/0
932	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA ,	01/2019	1,137.42 -	1,137.42	306.04	- -	-	-	0/0
933	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA ,	01/2019	1,033.19 -	1,033.19	209.75	- -	-	-	0/0
934	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA ,	01/2019	1,243.45 -	1,243.45	405.84	- -	-	-	0/0
935	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA ,	01/2019	889.36 -	889.36	284.69	- -	-	-	0/0
936	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA ,	01/2019	1,018.79 -	1,018.79	267.69	- -	-	-	0/0
937	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA ,	01/2019	996.65 -	996.65	350.94	- -	-	-	0/0
938	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH , PPP (BOT)	11/2013	1,916.79 -	1,916.79	1,948.92	11/2016 -	-	-	0/0
939	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH ,	09/2015	934.46 -	934.46	586.91	03/2018 -	03/2020	24(O) -	0/0
940	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH ,	02/2016	273.20 725.87	273.20	662.86	02/2019 -	06/2019	-	0/0
941	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH ,	08/2016	1,583.18 -	1,583.18	271.06	- -	09/2020	- -	0/0
942	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH ,	09/2016	1,273.71 -	1,273.71	581.40	- -	07/2020	- -	0/0
943	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH ,	10/2016	447.75 -	447.75	1,028.99	- -	08/2020	- -	0/0
944	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH ,	06/2017	2,485.93 -	2,485.93	596.94	06/2020 -	09/2021	15(O) -	0/0
945	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050 ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH ,	03/2018	478.74 -	478.74	55.06	- -	05/2021	- -	0/0
946	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,987.00 -	1,987.00	2,913.83	07/2015 12/2019	09/2020	62(O) 0	0/0
947	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	05/2011	2,159.00 -	2,519.00	4,707.04	06/2015 -	-	-	0/0
948	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,813.76 -	1,813.76	2,393.99	07/2013 -	-	-	0/0
949	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	06/2011	1,100.70 -	1,100.70	2,898.41	06/2014 09/2017	10/2020	76(O) 0	0/0
950	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR ,	12/2015	2,168.66 -	2,168.66	704.09	06/2019 -	12/2020	18(O) -	0/0
951	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR ,	12/2015	2,136.97 -	2,136.97	1,248.94	12/2018 -	07/2020	19(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
952	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR ,	12/2017	1,471.75 1,339.00	1,339.00	588.87	- -	01/2021	- -	1/3
953	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866]NHIDCL,JAMMU AND KASHMIR ,	03/2018	404.17 -	404.17	53.66	08/2018 -	-	-	2/4
954	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM - [N24000867]NHIDCL,JAMMU AND KASHMIR ,	03/2018	216.00 -	216.00	21.23	11/2018 -	-	-	0/4
955	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR ,	03/2018	253.44 -	253.44	.00	07/2019 -	-	-	0/0
956	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND , PPP (ANNUITY)	12/2012	1,479.00 -	1,479.00	740.26	06/2015 -	-	-	0/0
957	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND ,	02/2016	997.15 -	997.15	728.62	03/2019 -	-	-	0/0
958	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND ,	07/2016	458.03 -	458.03	338.86	- 12/2017	12/2019	-	0/0
959	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND ,	08/2016	323.72 -	323.72	232.58	08/2018 -	01/2020	17(O) -	0/0
960	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]NHAI,JHARKHAND ,	03/2017	165.50 -	172.16	117.09	03/2020 -	03/2020	0(O) -	0/0
961	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI,JHARKHAND ,	03/2017	239.68 -	235.90	91.24	03/2020 -	03/2020	0(O) -	0/0
962	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND ,	01/2018	273.46 -	273.46	.00	- -	-	-	0/0
963	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND ,	01/2018	1,155.16 -	1,155.16	30.13	- -	-	-	0/0
964	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND ,	03/2018	1,005.08 1,073.10	1,005.08	.00	- 03/2019	03/2021	- 0	0/0
965	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131]MoRTH,JHARKHAND ,	03/2018	212.99 -	212.99	99.21	06/2020 -	06/2020	0(O) -	0/0
966	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I - [N24001216]MoRTH,JHARKHAND ,	12/2016	196.00 -	196.00	.00	09/2021 -	09/2021	0(O) -	0/0
967	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA ,	09/2010	946.00 -	946.00	818.53	06/2018 -	12/2019	-	3/3
968	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA , EPC	03/2015	165.67 -	165.67	.00	11/2015 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
969	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MoRTH,KARNATAKA , EPC	03/2015	159.12 -	159.12	.00	11/2015 -	-	-	0/0
970	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MoRTH,KARNATAKA , EPC	01/1991	219.40 -	219.40	.00	01/2018 -	-	-	0/0
971	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA , PPP (BOT)	05/2014	1,655.01 -	1,655.01	1,867.51	08/2016 -	12/2020	52(O) -	0/0
972	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA , PPP (BOT)	03/2015	1,388.00 -	1,388.00	1,203.00	08/2018 -	03/2020	19(O) -	0/0
973	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA ,	03/2016	701.40 -	701.40	29.48	03/2019 -	11/2020	20(O) -	0/0
974	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA ,	03/2016	870.00 -	870.00	36.30	03/2019 -	11/2020	20(O) -	0/0
975	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA ,	08/2016	1,664.20 -	1,664.20	794.87	04/2020 -	04/2020	0(O) -	0/0
976	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA ,	08/2016	1,167.42 870.00	870.00	265.48	03/2019 03/2017	08/2020	17(O) 0	0/0
977	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA ,	09/2016	950.69 1,008.00	1,108.00	1,399.33	08/2019 -	12/2020	16(O) -	0/0
978	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA ,	03/2017	831.58 -	1,177.00	702.31	03/2020 -	07/2020	4(O) -	0/0
979	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O) - [N24000675]NHAI,KARNATAKA ,	03/2017	993.16 -	1,434.00	765.31	03/2020 -	06/2020	3(O) -	0/0
980	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA ,	02/2018	486.78 -	486.78	144.22	- -	-	-	0/0
981	SIX-LANING OF BANGALORE – NIDAGATTA SECTION KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA ,	02/2018	1,995.34 2,190.00	2,400.00	1,740.36	- 05/2019	11/2021	- 0	0/0
982	SIX LANING OF NIDAGATTA-MYSORE SECTION KM 74.20 TO KM 135.304 OF NH-275 IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA ,	02/2018	2,177.80 2,283.50	2,450.00	931.86	- 10/2019	-	-	0/0
983	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT - [N24001154]MoRTH,KARNATAKA ,	08/2016	367.44 -	367.44	61.95	01/2017 -	-	-	0/0
984	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT - [N24001155]MoRTH,KARNATAKA ,	08/2016	175.20 -	175.20	113.38	01/2017 -	-	-	0/0
985	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA - [N24001156]MoRTH,KARNATAKA ,	01/2017	166.67 -	166.67	117.05	09/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
986	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA ,	08/2016	175.50 -	175.50	86.54	02/2017 -	-	-	0/0
987	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA ,	03/2018	159.97 -	159.97	.00	06/2019 -	-	-	0/0
988	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]MoRTH,KARNATAKA ,	01/2018	159.70 -	159.70	22.79	07/2018 -	-	-	0/0
989	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA ,	09/2017	191.60 -	191.60	26.24	10/2018 -	-	-	0/0
990	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- [N24001161]MoRTH,KARNATAKA ,	12/2017	297.30 -	297.30	.00	01/2019 -	-	-	0/0
991	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA ,	03/2018	325.86 -	325.86	62.54	10/2018 -	-	-	0/0
992	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]MoRTH,KARNATAKA ,	08/2016	329.01 -	329.01	135.50	02/2017 -	-	-	0/0
993	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA ,	10/2016	396.96 -	396.96	113.98	03/2017 -	-	-	0/0
994	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA ,	11/2016	314.90 -	314.90	104.40	03/2017 -	-	-	0/0
995	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA ,	03/2015	159.12 -	159.12	96.22	01/2016 -	-	-	0/0
996	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776) - [N24001167]MoRTH,KARNATAKA ,	03/2015	165.67 -	165.67	87.63	01/2016 -	-	-	0/0
997	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA ,	05/2018	171.60 -	171.60	.86	05/2018 -	05/2020	24(O) -	0/0
998	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM. - [N24001170]MoRTH,KARNATAKA ,	01/2014	471.16 -	471.16	128.32	08/2014 -	-	-	0/0
999	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA ,	01/2017	291.49 -	291.49	130.00	08/2017 -	-	-	0/0
1000	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA ,	02/2017	157.32 188.00	157.32	.00	05/2019 -	05/2021	24(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1001	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA , PPP (BOT)	02/2010	617.00 -	617.00	943.17	08/2012 -	12/2019	-	0/0
1002	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]MoRTH,KERALA , EPC	01/2014	255.75 348.00	348.43	290.12	09/2017 -	-	-	0/0
1003	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA ,	06/2015	845.24 -	941.00	859.59	- -	01/2020	- -	0/0
1004	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA ,	04/2016	804.97 -	804.97	465.05	06/2018 -	03/2020	21(O) -	0/0
1005	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA , Central Sector Projects	09/2017	1,124.11 -	1,232.76	314.14	09/2017 -	05/2021	44(O) -	0/0
1006	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA ,	02/2018	1,424.77 -	1,853.42	14.19	- -	-	-	0/0
1007	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH , PPP (BOT)	10/2010	1,175.00 -	1,175.00	1,509.96	04/2013 -	-	-	4/4
1008	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH , PPP (BOT)	11/2010	325.00 -	475.00	469.54	05/2013 -	-	-	3/3
1009	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]MoRTH,MADHYA PRADESH , BOT (TOLL)	01/2012	320.48 -	320.48	189.49	08/2015 -	-	-	0/0
1010	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH,MADHYA PRADESH , EPC	06/2015	390.51 -	390.51	209.67	- -	03/2020	- -	0/0
1011	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]MoRTH,MADHYA PRADESH , EPC	11/2013	497.05 -	881.05	624.54	05/2017 -	05/2020	36(O) -	0/0
1012	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]MoRTH,MADHYA PRADESH , BOT (TOLL)	08/2015	257.80 -	257.00	12.38	- -	-	-	0/0
1013	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]MoRTH,MADHYA PRADESH , BOT (TOLL)	11/2011	954.43 1,191.51	1,191.51	235.61	09/2015 -	10/2021	73(O) -	0/0
1014	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH , BOT (TOLL)	01/2012	410.72 -	410.72	390.00	04/2015 -	10/2019	-	0/0
1015	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH ,	03/2015	795.76 659.57	677.72	659.57	- -	03/2020	- -	0/0
1016	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH ,	03/2015	794.30 637.86	691.38	637.86	- -	12/2019	-	0/0
1017	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH , EPC	11/2015	628.45 -	628.45	300.52	01/2020 -	09/2020	8(O) -	0/0
1018	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]MoRTH,MADHYA PRADESH , EPC	12/2015	957.54 -	957.54	573.28	02/2020 -	08/2020	6(O) -	0/0
1019	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH ,	03/2015	928.83 -	928.83	709.38	- 06/2015	06/2015	-	0/0
1020	FOUR LANING OF GWALIOR-SHIPURI - [N24000494]NHAI,MADHYA PRADESH , PPP (BOT)	05/2013	1,055.00 -	1,601.77	1,393.40	11/2015 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1021	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH ,	06/2015	1,012.90 -	1,012.90	226.10	03/2016 -	-	-	0/0
1022	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH ,	03/2015	810.22 -	810.22	721.55	- 06/2015	06/2015	-	0/0
1023	FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH , PPP (BOT)	06/2015	1,583.79 -	1,583.79	1,648.90	01/2019 10/2019	10/2019	-	0/3
1024	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH,MADHYA PRADESH , EPC	03/2015	511.83 -	511.83	278.88	08/2017 -	02/2020	30(O) -	0/0
1025	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH ,	08/2016	227.49 -	227.49	129.93	01/2019 -	12/2019	-	3/4
1026	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH , Central Sector Projects	10/2017	639.97 -	639.97	331.84	10/2017 -	01/2020	27(O) -	2/4
1027	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	374.40 -	204.65	155.83	09/2017 -	-	-	3/4
1028	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	990.61 -	990.61	397.89	09/2017 -	01/2021	40(O) -	0/4
1029	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH ,	12/2017	950.27 -	950.27	168.05	- -	-	-	2/4
1030	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH ,	01/2018	960.24 -	960.24	328.34	- -	-	-	0/0
1031	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI,MADHYA PRADESH ,	01/2018	770.73 -	770.73	59.45	- -	-	-	0/0
1032	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH ,	03/2018	162.56 -	162.56	119.50	03/2018 -	05/2020	26(O) -	0/0
1033	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH ,	03/2018	166.21 -	166.21	67.45	08/2018 -	06/2020	22(O) -	0/0
1034	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH,MADHYA PRADESH ,	02/2018	169.63 -	169.63	14.67	03/2018 -	07/2020	28(O) -	0/0
1035	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]MoRTH,MADHYA PRADESH ,	11/2017	235.91 -	235.91	156.89	02/2018 -	05/2020	27(O) -	0/0
1036	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]MoRTH,MADHYA PRADESH ,	11/2017	184.62 -	184.62	76.60	02/2018 -	05/2020	27(O) -	0/0
1037	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884]MoRTH,MADHYA PRADESH ,	03/2018	191.21 -	191.21	78.35	11/2019 -	05/2020	6(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1038	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH ,	01/2017	205.05 -	205.05	85.57	03/2017 -	09/2020	42(O) -	0/0
1039	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH ,	03/2018	214.69 -	214.69	30.44	03/2018 -	12/2020	33(O) -	0/0
1040	UPGRADATION OF PORSABHIND ROAD TO 2L + PS - [N24000890]MoRTH,MADHYA PRADESH ,	03/2018	217.22 226.88	226.88	86.83	08/2018 -	06/2020	22(O) -	0/0
1041	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH ,	03/2018	233.04 -	233.04	131.22	03/2018 -	04/2020	25(O) -	0/0
1042	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH ,	11/2017	249.05 -	249.05	143.64	07/2018 -	06/2020	23(O) -	0/0
1043	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]MoRTH,MADHYA PRADESH ,	11/2017	254.17 -	254.17	157.83	02/2018 -	09/2020	31(O) -	0/0
1044	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH ,	02/2018	279.44 -	279.44	76.00	03/2018 -	04/2020	25(O) -	0/0
1045	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 - [N24000895]MoRTH,MADHYA PRADESH ,	09/2016	287.34 -	287.34	158.05	01/2019 -	03/2020	14(O) -	0/0
1046	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]MoRTH,MADHYA PRADESH ,	01/2017	373.82 -	373.82	143.05	09/2019 -	09/2020	12(O) -	0/0
1047	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]MoRTH,MADHYA PRADESH ,	01/2016	809.16 -	809.16	353.90	07/2018 -	09/2020	26(O) -	0/0
1048	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]MoRTH,MADHYA PRADESH ,	03/2016	877.79 -	877.79	467.48	06/2019 -	07/2020	13(O) -	0/0
1049	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 - [N24000962]MoRTH,MADHYA PRADESH ,	09/2016	178.23 -	178.23	122.99	09/2018 -	08/2019	-	0/0
1050	ANJANGAON TO MAH/MP BORDER - [N24001007]MoRTH,MADHYA PRADESH ,	01/2017	359.00 359.00	359.00	221.80	06/2019 -	-	-	0/4
1051	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MoRTH,MADHYA PRADESH ,	11/2017	392.33 428.55	428.55	253.99	03/2018 -	09/2020	30(O) -	0/0
1052	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]MoRTH,MADHYA PRADESH ,	01/2019	264.50 -	264.50	.00	03/2021 -	03/2021	0(O) -	0/0
1053	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI,MADHYA PRADESH ,	10/2019	743.88 -	743.88	.00	- -	-	-	0/0
1054	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]NHAI,MADHYA PRADESH ,	12/2017	656.98 -	656.98	2.48	- -	-	-	0/0
1055	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA - [N24001213]NHAI,MADHYA PRADESH ,	12/2017	1,094.97 -	1,094.97	1.51	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1056	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214]NHAI,MADHYA PRADESH ,	12/2017	217.96 -	217.96	.50	- -	-	-	0/0
1057	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA , PPP (BOT)	10/2010	1,724.55 -	1,724.55	2,442.58	03/2013 -	03/2020	84(O) -	0/0
1058	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA , PPP (BOT)	05/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	-	-	2/2
1059	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]MoRTH,MAHARASHTRA , EPC	03/2015	168.30 -	168.30	80.00	- -	-	-	0/4
1060	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]MoRTH,MAHARASHTRA , EPC	08/2014	187.79 -	187.79	76.62	07/2016 -	-	-	0/12
1061	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]MoRTH,MAHARASHTRA , EPC	01/2014	446.77 -	446.77	278.50	- -	-	-	3/4
1062	WIDENING NH-848 FROM KM 16.000 TO 34.000 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MoRTH,MAHARASHTRA , EPC	10/2015	289.60 -	289.60	90.65	- -	-	-	0/0
1063	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MoRTH,MAHARASHTRA , ITEM RATE	12/2011	156.26 227.00	247.95	175.00	- -	-	-	0/0
1064	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA , EPC	01/2015	225.81 -	225.81	85.11	- -	-	-	0/0
1065	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	2,288.18 -	2,288.18	487.81	05/2019 -	-	-	0/0
1066	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA ,	09/2015	414.51 414.00	414.00	543.46	05/2018 05/2020	05/2020	24(O) 0	0/1
1067	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA ,	10/2015	531.13 -	727.00	524.15	05/2018 -	09/2020	28(O) -	0/0
1068	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA , EPC	07/2015	1,885.74 -	1,885.74	1,636.02	05/2019 -	-	-	0/0
1069	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA ,	10/2015	593.26 41.54	636.24	490.35	05/2018 06/2020	06/2020	25(O) 0	0/1
1070	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB SERVICE ROADS FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA ,	12/2015	649.50 -	649.50	155.81	03/2019 04/2021	04/2021	25(O) 0	0/0
1071	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA ,	08/2015	505.00 -	504.00	241.74	05/2018 04/2019	09/2020	28(O) 0	0/1
1072	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA , PPP (BOT)	01/2015	972.50 -	972.50	1,492.00	07/2017 12/2019	03/2020	32(O) 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1073	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA , PPP (BOT)	06/2014	923.04 -	923.04	767.17	11/2016 -	05/2020	42(O) -	0/0
1074	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	1,871.34 67.34	1,871.34	3,544.79	01/2018 12/2018	03/2020	26(O) 3	0/0
1075	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA ,	04/2010	1,170.52 -	1,170.52	2,051.36	06/2012 -	-	-	0/0
1076	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA ,	03/2016	197.69 151.11	197.69	151.11	07/2018 -	-	-	0/0
1077	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA ,	03/2016	546.00 -	546.00	269.67	07/2019 12/2020	12/2020	17(O) 0	0/0
1078	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA ,	03/2016	591.66 -	591.66	310.56	07/2019 12/2020	12/2020	17(O) 0	0/0
1079	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH,MAHARASHTRA ,	03/2016	1,142.62 -	1,142.62	836.85	- -	-	-	0/0
1080	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH,MAHARASHTRA ,	03/2016	1,101.58 -	1,101.58	315.00	- -	-	-	0/0
1081	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA ,	11/2016	1,071.61 -	1,048.10	514.46	- -	07/2021	- -	2/4
1082	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA ,	11/2016	1,064.88 -	1,021.00	124.00	- -	07/2021	- -	0/4
1083	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA ,	11/2016	400.25 -	400.25	64.89	03/2019 -	02/2021	23(O) -	0/0
1084	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA ,	11/2016	446.17 -	446.17	38.97	03/2019 -	03/2021	24(O) -	0/0
1085	SIX LANNING FROM EXISTING KM 494.410(DSIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DSIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA ,	11/2016	290.73 315.00	315.00	246.70	- 03/2020	03/2020	- 12	0/0
1086	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA ,	01/2017	244.90 -	244.90	251.87	05/2019 -	12/2019	-	0/0
1087	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA ,	02/2017	904.16 911.07	904.16	855.25	02/2020 11/2017	05/2020	3(O) 0	0/0
1088	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA ,	03/2017	247.02 -	157.49	31.97	03/2020 02/2021	02/2020	-1(O) 0	0/0
1089	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA ,	03/2017	744.64 -	982.00	.00	03/2020 -	03/2020	0(O) -	0/0
1090	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA ,	03/2017	1,030.44 -	1,065.51	1,015.76	03/2020 -	05/2020	2(O) -	0/3
1091	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA ,	03/2017	988.34 988.00	1,043.28	1,035.00	03/2020 -	08/2020	5(O) -	3/3

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1092	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA ,	03/2017	1,059.73 -	1,071.00	610.87	03/2017 05/2018	11/2020	44(O) 0	0/0
1093	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA ,	03/2017	296.19 -	254.00	254.85	03/2020 -	03/2020	0(O) -	0/0
1094	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA ,	03/2017	1,098.06 -	1,160.64	1,068.76	03/2020 -	08/2020	5(O) -	0/3
1095	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA ,	12/2017	404.94 448.18	448.18	193.77	- -	10/2020	- -	0/0
1096	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA ,	01/2018	607.00 512.99	607.00	187.53	- 02/2019	08/2021	- 0	0/1
1097	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA ,	01/2018	621.00 565.02	621.00	383.83	- 10/2018	04/2021	- 0	2/3
1098	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA , EPC	03/2018	291.53 -	291.53	68.92	- 11/2020	11/2020	- 0	0/0
1099	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA , EPC	03/2018	289.21 -	289.21	41.34	- -	11/2020	- -	0/0
1100	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA ,	03/2018	1,162.92 -	1,162.92	15.36	- -	07/2021	- -	0/0
1101	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA ,	03/2018	642.13 -	807.00	395.79	- -	12/2020	- -	0/0
1102	SARSAM TO KOTHARI - [N24001002]MoRTH,MAHARASHTRA ,	02/2016	545.64 -	545.64	113.53	07/2019 -	-	-	0/4
1103	AKOLA TO AKOT - [N24001003]MoRTH,MAHARASHTRA ,	01/2017	313.95 -	313.95	48.24	06/2019 -	-	-	0/4
1104	AKOT TO ANJANGAON - [N24001006]MoRTH,MAHARASHTRA ,	01/2017	245.77 246.00	245.77	158.98	06/2019 -	-	-	0/4
1105	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA ,	02/2017	203.21 203.00	203.21	146.79	05/2019 -	12/2019	-	0/0
1106	SHEGAON TO DEORI PHATA - [N24001010]MoRTH,MAHARASHTRA ,	02/2017	373.10 373.00	373.10	163.43	05/2019 -	12/2019	-	0/4
1107	MEHKAR TO CHIKALI - [N24001011]MoRTH,MAHARASHTRA ,	02/2017	322.48 322.00	322.48	229.08	05/2019 -	-	-	0/4
1108	CHIKALI TO KHAMGAON - [N24001012]MoRTH,MAHARASHTRA ,	02/2017	548.03 548.00	548.03	319.00	06/2019 -	10/2019	-	0/4
1109	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA ,	01/2017	391.06 391.00	391.06	147.00	06/2019 -	06/2020	12(O) -	0/0
1110	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA ,	01/2017	385.87 386.00	385.87	232.75	06/2019 -	12/2019	-	0/0
1111	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA ,	01/2017	341.16 341.00	341.16	191.29	06/2019 -	-	-	0/0
1112	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH,MAHARASHTRA ,	01/2017	471.61 472.00	471.61	288.90	06/2019 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1113	DAHEGAON TO KUHI - [N24001017]MoRTH,MAHARASHTRA ,	01/2017	228.89 229.00	228.89	130.00	06/2019 -	-	-	3/4
1114	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA ,	01/2017	392.83 393.00	392.83	286.60	06/2019 -	-	-	0/0
1115	KATOL TO WARUD - [N24001019]MoRTH,MAHARASHTRA ,	01/2017	463.62 664.00	463.62	241.34	06/2019 -	08/2019	-	0/4
1116	AMDIT TO SAONER - [N24001021]MoRTH,MAHARASHTRA ,	01/2017	396.91 396.91	396.91	254.48	06/2019 -	08/2019	-	3/4
1117	WADI TO ASOLA - [N24001022]MoRTH,MAHARASHTRA ,	01/2017	363.82 363.82	363.82	92.10	09/2019 -	09/2020	12(O) -	1/4
1118	NAGAJ TO VAJJAPUR - [N24001023]MoRTH,MAHARASHTRA ,	01/2017	376.72 377.00	376.72	183.81	06/2019 -	12/2019	-	0/4
1119	MANGAON TO DIGHI PORT - [N24001024]MoRTH,MAHARASHTRA ,	01/2017	457.52 457.52	457.52	277.98	07/2019 -	07/2020	12(O) -	2/4
1120	INDAPUR TO AGARDANDA - [N24001025]MoRTH,MAHARASHTRA ,	01/2017	355.17 -	355.17	169.87	07/2019 -	12/2019	-	3/4
1121	WAKAN PALI KHOPOLI - [N24001026]MoRTH,MAHARASHTRA ,	01/2017	376.19 376.19	376.19	37.03	05/2019 -	05/2020	12(O) -	1/4
1122	SHAHUPUR PATGAON SECTION I - [N24001027]MoRTH,MAHARASHTRA ,	01/2018	150.79 150.79	150.79	21.42	12/2019 -	12/2019	-	1/4
1123	PATGAON KHOPOLI SECTION I - [N24001028]MoRTH,MAHARASHTRA ,	01/2018	170.00 -	170.00	56.57	12/2019 -	12/2019	-	0/4
1124	AHMADPUR TO PIMPLA - [N24001029]MoRTH,MAHARASHTRA ,	01/2017	422.38 422.38	422.38	161.58	08/2019 -	08/2019	-	2/4
1125	PIMPLA TO MANJARSUMBHA - [N24001030]MoRTH,MAHARASHTRA ,	01/2017	595.77 595.77	595.77	171.44	08/2019 -	08/2019	-	2/4
1126	MANJUSUMBA TO CHUMBALI - [N24001031]MoRTH,MAHARASHTRA ,	01/2017	228.54 228.54	228.54	107.30	08/2019 -	08/2019	-	2/4
1127	DEORI TO AMGAON - [N24001032]MoRTH,MAHARASHTRA ,	01/2017	409.62 410.00	409.62	181.78	05/2019 -	05/2020	12(O) -	0/4
1128	MANTHA TALUKAS BORDER TO PARTUR - [N24001033]MoRTH,MAHARASHTRA ,	01/2017	486.19 486.19	486.19	235.55	07/2019 -	07/2019	-	2/4
1129	PARTUR TO MAJALGAON - [N24001034]MoRTH,MAHARASHTRA ,	01/2017	420.57 420.57	420.57	186.39	07/2019 -	07/2019	-	2/4
1130	MANSAR TO SALAIKHURD - [N24001035]MoRTH,MAHARASHTRA ,	01/2018	418.36 -	418.36	142.13	12/2019 -	12/2019	-	0/4
1131	MAJALGAON TO KAIJ - [N24001036]MoRTH,MAHARASHTRA ,	01/2017	413.99 -	413.99	299.33	07/2019 -	07/2019	-	0/0
1132	KAIJ TO KUSALAM - [N24001037]MoRTH,MAHARASHTRA ,	01/2017	554.78 554.78	554.78	184.90	07/2019 -	07/2019	-	2/4
1133	MAHAD TO RAIGAD FORT - [N24001038]MoRTH,MAHARASHTRA ,	07/2018	237.40 -	237.40	8.34	05/2020 -	05/2020	0(O) -	0/4
1134	JINTUR TO PARBHANI - [N24001039]MoRTH,MAHARASHTRA ,	01/2017	356.66 356.66	356.66	49.88	- -	-	-	0/4
1135	JAHIRABAD TO LATUR - [N24001040]MoRTH,MAHARASHTRA ,	01/2017	461.96 461.96	461.96	170.43	11/2019 -	11/2019	-	2/4
1136	SHIROD SHAHPURER TO NANDED - [N24001041]MoRTH,MAHARASHTRA ,	01/2017	211.34 211.34	211.34	104.83	07/2019 -	07/2019	-	2/4
1137	SALAIKHURD TO TIRORA - [N24001042]MoRTH,MAHARASHTRA ,	01/2018	415.25 415.25	415.25	111.22	12/2019 -	12/2019	-	0/4
1138	NILAJPHATA TO BHANDARA - [N24001043]MoRTH,MAHARASHTRA ,	01/2018	420.63 421.00	420.63	50.60	05/2020 -	05/2020	0(O) -	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1139	KALMAB TO RALEGAON - [N24001044]MoRTH,MAHARASHTRA ,	01/2017	467.78 -	467.78	301.91	06/2019 -	-	-	0/4
1140	JALGAON TO BHADGAON - [N24001045]MoRTH,MAHARASHTRA ,	01/2018	307.54 308.00	307.54	159.59	11/2019 -	11/2019	-	0/4
1141	RALEGAON TO RAMTIRTH - [N24001046]MoRTH,MAHARASHTRA ,	01/2017	210.81 -	210.81	120.69	07/2019 -	-	-	0/4
1142	BHADGAON TO CHALISGAON - [N24001047]MoRTH,MAHARASHTRA ,	01/2018	259.55 260.00	259.55	182.24	11/2019 -	11/2019	-	0/0
1143	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA ,	01/2017	232.77 -	232.77	92.51	07/2019 -	-	-	0/0
1144	KARAD TO VITA - [N24001049]MoRTH,MAHARASHTRA ,	01/2018	344.85 245.00	344.85	98.86	12/2019 -	12/2019	-	0/4
1145	VITA TO NAGAJ - [N24001050]MoRTH,MAHARASHTRA ,	03/2018	304.58 305.00	304.58	24.82	12/2019 -	12/2019	-	0/4
1146	NALDURG TO AKKALKOT - [N24001051]MoRTH,MAHARASHTRA ,	02/2018	274.50 275.00	274.50	66.39	12/2019 -	12/2019	-	0/4
1147	SANGOLA TO JATH - [N24001052]MoRTH,MAHARASHTRA ,	01/2018	257.38 257.00	257.38	94.15	12/2019 -	12/2019	-	0/4
1148	KARAD TO TAGAON - [N24001053]MoRTH,MAHARASHTRA ,	01/2017	537.81 538.00	537.81	98.97	06/2019 -	06/2020	12(O) -	0/4
1149	TASGAON TO SHIRDHON - [N24001054]MoRTH,MAHARASHTRA ,	01/2017	195.64 196.00	195.64	169.73	11/2019 -	11/2019	-	0/4
1150	HELWAK TO KARAD - [N24001055]MoRTH,MAHARASHTRA ,	02/2017	416.99 -	416.99	132.40	07/2019 -	-	-	0/4
1151	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA ,	02/2017	422.02 422.00	422.02	247.01	07/2019 -	-	-	0/0
1152	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MoRTH,MAHARASHTRA ,	02/2017	407.19 407.00	407.19	25.00	06/2019 -	06/2020	12(O) -	0/4
1153	KARWANDI TO RAJURI - [N24001058]MoRTH,MAHARASHTRA ,	03/2018	276.95 277.00	276.95	107.47	12/2019 -	12/2019	-	0/4
1154	SHIVUR TO YEOLA - [N24001059]MoRTH,MAHARASHTRA ,	03/2018	181.08 -	181.08	7.50	12/2019 -	12/2019	-	0/4
1155	PALPHATA TO PHULAMBARI - [N24001060]MoRTH,MAHARASHTRA ,	03/2018	227.19 227.00	227.19	80.23	12/2019 -	12/2019	-	0/4
1156	CHIKALI TO DHAD - [N24001061]MoRTH,MAHARASHTRA ,	03/2018	189.46 189.00	189.46	35.54	12/2019 -	12/2019	-	0/4
1157	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]MoRTH,MAHARASHTRA ,	03/2018	336.21 336.00	336.21	78.66	12/2019 -	12/2019	-	0/4
1158	WADIGODRI TO DHANGRIPIMPRI - [N24001063]MoRTH,MAHARASHTRA ,	03/2018	194.23 194.00	194.23	88.23	02/2020 -	02/2020	0(O) -	0/4
1159	DHANGRIPIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]MoRTH,MAHARASHTRA ,	03/2018	217.14 217.00	217.14	100.77	02/2020 -	02/2020	0(O) -	0/4
1160	PARBHANI TO GANGKHED - [N24001065]MoRTH,MAHARASHTRA ,	03/2018	238.19 238.00	238.19	56.85	12/2019 -	12/2019	-	0/4
1161	LATUR TO PANGAON - [N24001066]MoRTH,MAHARASHTRA ,	03/2018	336.47 336.00	336.47	142.18	12/2019 -	12/2019	-	0/4
1162	OMREGA TO AUSA - [N24001067]MoRTH,MAHARASHTRA ,	03/2018	272.04 272.00	272.04	164.24	12/2019 -	12/2019	-	0/4
1163	WASHIM TO DASTAPUR - [N24001068]MoRTH,MAHARASHTRA ,	03/2018	165.51 -	165.51	83.45	12/2019 -	12/2019	-	1/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1164	NANDED TO JALKOT - [N24001069]MoRTH,MAHARASHTRA ,	12/2017	456.93 457.00	456.93	87.95	09/2019 -	09/2019	-	1/4
1165	DASTAPUR TO KARANJA - [N24001070]MoRTH,MAHARASHTRA ,	03/2018	182.63 -	182.63	114.40	12/2019 -	12/2019	-	2/4
1166	JALKOT TO TOGRI - [N24001071]MoRTH,MAHARASHTRA ,	07/2018	299.92 300.00	299.92	19.25	08/2020 -	08/2020	0(O) -	0/4
1167	KHERDA TO NAGZARI - [N24001072]MoRTH,MAHARASHTRA ,	03/2018	181.30 -	181.30	111.50	12/2019 -	12/2019	-	0/4
1168	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA ,	09/2018	301.38 301.00	301.38	59.42	08/2020 -	08/2020	0(O) -	0/0
1169	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA ,	03/2018	249.29 -	249.29	116.20	12/2019 -	12/2019	-	0/0
1170	OSMANNAGAR TO KUNDAL - [N24001075]MoRTH,MAHARASHTRA ,	09/2017	344.25 344.00	344.25	71.18	08/2020 -	08/2020	0(O) -	0/4
1171	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA ,	03/2018	219.91 -	219.91	123.76	12/2019 -	12/2019	-	0/0
1172	KUNDAL TO WAZAR - [N24001077]MoRTH,MAHARASHTRA ,	01/2018	225.25 225.00	225.25	163.75	12/2019 -	12/2019	-	2/4
1173	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA ,	03/2018	228.31 -	228.31	19.50	12/2019 -	12/2019	-	0/0
1174	ARDHAPUR TO HIMAYATNAGAR - [N24001079]MoRTH,MAHARASHTRA ,	12/2017	426.06 426.00	426.06	91.97	06/2020 -	06/2020	0(O) -	1/4
1175	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA ,	03/2018	256.15 -	256.15	43.50	12/2019 -	12/2019	-	0/0
1176	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]MoRTH,MAHARASHTRA ,	03/2018	294.87 295.00	294.87	54.30	12/2019 -	12/2019	-	1/4
1177	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA ,	03/2018	223.46 -	223.46	21.42	12/2019 -	12/2019	-	0/0
1178	CHIKLI TO TAKARKHED - [N24001083]MoRTH,MAHARASHTRA ,	03/2018	393.10 393.10	393.10	166.97	12/2019 -	12/2019	-	2/4
1179	PAHUR TO BODHWAD - [N24001084]MoRTH,MAHARASHTRA ,	01/2017	244.93 -	244.93	75.23	05/2020 -	05/2020	0(O) -	0/4
1180	TAKARKHED TO JALNA - [N24001085]MoRTH,MAHARASHTRA ,	09/2017	417.90 418.00	417.90	138.26	06/2019 -	12/2019	-	0/4
1181	BODHWAD TO STATE BORDER - [N24001086]MoRTH,MAHARASHTRA ,	01/2017	178.26 -	178.26	124.95	07/2019 -	-	-	0/4
1182	MANGRUPHIR TO MAHAN - [N24001087]MoRTH,MAHARASHTRA ,	03/2018	222.13 222.13	222.13	96.63	11/2019 -	11/2019	-	0/4
1183	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA ,	03/2018	177.84 177.00	177.84	73.69	12/2019 -	12/2019	-	0/0
1184	MALEGAON TO RISOD - [N24001089]MoRTH,MAHARASHTRA ,	02/2018	303.24 303.24	303.24	138.97	12/2019 -	12/2019	-	0/4
1185	KOLDE TO KHETIYA - [N24001090]MoRTH,MAHARASHTRA ,	01/2017	509.18 -	509.18	205.93	07/2019 -	-	-	0/4
1186	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]MoRTH,MAHARASHTRA ,	03/2016	536.65 356.00	536.65	472.99	12/2019 -	12/2019	-	0/0
1187	SATARA TO MHASWAD - [N24001092]MoRTH,MAHARASHTRA ,	01/2017	653.46 -	653.46	240.42	07/2019 -	-	-	0/4
1188	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA ,	12/2017	309.94 310.00	309.94	71.32	12/2019 -	12/2019	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1189	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA ,	12/2017	244.04 244.00	244.04	44.94	03/2019 -	12/2019	-	0/0
1190	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA ,	01/2017	388.44 -	388.44	191.77	- -	-	-	0/0
1191	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA ,	01/2018	264.41 264.00	264.41	53.71	03/2019 -	12/2019	-	0/0
1192	SELDOH TO PANVAR - [N24001097]MoRTH,MAHARASHTRA ,	07/2018	404.33 404.00	404.33	44.19	05/2020 -	05/2020	0(O) -	0/4
1193	WARDHA TO HINGAGHAT - [N24001098]MoRTH,MAHARASHTRA ,	01/2018	216.90 216.90	216.90	82.54	12/2019 -	12/2019	-	1/4
1194	MHASWAD TO TEMBHURNI - [N24001099]MoRTH,MAHARASHTRA ,	01/2017	488.60 -	488.60	213.71	07/2019 -	-	-	0/4
1195	AHMEDNAGAR TO BARAMATI - [N24001100]MoRTH,MAHARASHTRA ,	01/2017	955.40 -	955.40	385.50	08/2019 -	08/2019	-	0/4
1196	KURUDWADI TO PANDHARPUR - [N24001101]MoRTH,MAHARASHTRA ,	01/2017	307.63 -	307.63	173.17	07/2019 -	-	-	0/4
1197	PANDHARPUR TO SANGOLA - [N24001102]MoRTH,MAHARASHTRA ,	07/2017	218.38 -	218.38	168.75	07/2019 -	-	-	0/4
1198	SARAD VANI PIMPALGAON - [N24001103]MoRTH,MAHARASHTRA ,	01/2017	250.46 -	250.46	107.63	07/2019 -	-	-	0/4
1199	MALEWADA TO CHIMUR - [N24001104]MoRTH,MAHARASHTRA ,	10/2016	322.55 -	322.55	184.91	06/2019 -	06/2020	12(O) -	2/4
1200	CHIMUR TO WARORA - [N24001105]MoRTH,MAHARASHTRA ,	11/2016	467.70 -	467.70	156.72	03/2019 -	-	-	0/4
1201	PEN TO KHOPOLI - [N24001106]MoRTH,MAHARASHTRA ,	03/2018	301.39 302.00	301.39	17.09	03/2018 -	12/2019	-	0/4
1202	PANCHARAL TO MANDANGHAR - [N24001107]MoRTH,MAHARASHTRA ,	07/2018	381.08 302.00	381.08	13.03	05/2020 -	05/2020	0(O) -	0/4
1203	CHALISGAON TO NANDGAON - [N24001108]MoRTH,MAHARASHTRA ,	03/2018	206.97 207.00	206.97	94.89	12/2019 -	12/2019	-	0/4
1204	KUSUMBA TO MALEGAON - [N24001109]MoRTH,MAHARASHTRA ,	03/2018	243.45 244.00	243.45	96.02	12/2019 -	12/2019	-	0/4
1205	BAMNI TO NAVEGAON - [N24001110]MoRTH,MAHARASHTRA ,	09/2017	241.69 242.00	241.69	109.29	04/2020 -	04/2020	0(O) -	1/4
1206	KOLHA TO NASRATPUR - [N24001111]MoRTH,MAHARASHTRA ,	04/2016	281.78 282.00	281.78	29.73	04/2019 -	04/2020	12(O) -	0/4
1207	NASRATPUR TO BARASGAON - [N24001112]MoRTH,MAHARASHTRA ,	07/2016	406.54 406.54	406.54	147.00	09/2019 -	09/2019	-	2/4
1208	BARASGAON TO RAHATEE - [N24001113]MoRTH,MAHARASHTRA ,	07/2016	289.11 290.00	289.11	33.82	09/2018 -	04/2021	31(O) -	0/4
1209	INDAPUR TO VADPALE - [N24001114]MoRTH,MAHARASHTRA ,	01/2017	1,202.52 1,202.52	1,202.52	635.90	12/2019 -	03/2020	3(O) -	1/4
1210	VADPALE TO BHOGAN KHURD - [N24001115]MoRTH,MAHARASHTRA ,	01/2017	1,598.47 1,560.00	1,598.47	768.91	11/2019 -	03/2020	4(O) -	1/4
1211	GADCHIROLI TO MUL - [N24001116]MoRTH,MAHARASHTRA ,	12/2016	484.15 -	484.15	162.31	06/2019 -	-	-	2/4
1212	MUL TO CHANDRAPUR - [N24001117]MoRTH,MAHARASHTRA ,	12/2016	162.34 -	162.34	32.80	07/2019 -	07/2019	-	1/4
1213	SAKOLI TO BHANDARA - [N24001118]MoRTH,MAHARASHTRA ,	01/2017	362.96 362.96	362.96	37.83	06/2019 -	11/2019	-	0/4
1214	NAGBHID TO ARMORI - [N24001119]MoRTH,MAHARASHTRA ,	09/2016	269.05 -	269.05	222.91	07/2019 -	-	-	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1215	AKKALKOT TO DHUDHNI - [N24001120]MoRTH,MAHARASHTRA ,	04/2016	211.42 -	211.42	131.85	02/2019 -	02/2020	12(O) -	0/4
1216	NASHIK TO PETH - [N24001121]MoRTH,MAHARASHTRA ,	12/2015	289.60 -	289.60	129.81	11/2018 -	11/2019	-	0/4
1217	PAITHAN TO SHIRUR - [N24001122]MoRTH,MAHARASHTRA ,	03/2017	341.80 -	341.80	107.89	06/2019 -	-	-	0/4
1218	SHIRUR TO KHARDA - [N24001123]MoRTH,MAHARASHTRA ,	02/2017	381.77 -	381.77	157.79	06/2019 -	-	-	0/4
1219	AURANGABAD TO SILLOD - [N24001124]MoRTH,MAHARASHTRA ,	02/2017	456.32 -	456.32	116.75	06/2019 -	-	-	0/4
1220	SILLOD TO FARDAPUR - [N24001125]MoRTH,MAHARASHTRA ,	02/2017	337.46 -	337.46	52.22	06/2019 -	-	-	0/4
1221	FARDAPUR TO JALGAON - [N24001126]MoRTH,MAHARASHTRA ,	02/2017	456.45 -	456.45	71.74	06/2019 -	-	-	0/4
1222	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA ,	02/2017	406.51 -	406.51	280.69	06/2019 -	-	-	0/0
1223	BHOKAR TO SARSAM - [N24001128]MoRTH,MAHARASHTRA ,	02/2017	295.09 -	295.99	179.64	07/2019 -	-	-	0/4
1224	BHOGAN KHURD TO KASHEDI - [N24001132]MoRTH,MAHARASHTRA ,	09/2017	743.21 743.00	743.21	131.87	06/2021 -	06/2021	0(O) -	1/4
1225	PARSHURAM GHAT TO ARAWALI - [N24001133]MoRTH,MAHARASHTRA ,	04/2016	983.14 983.00	983.14	655.15	12/2019 -	-	-	1/4
1226	KANTE TO WAKED - [N24001134]MoRTH,MAHARASHTRA ,	03/2016	1,230.02 1,230.00	1,230.02	566.61	11/2019 -	-	-	1/4
1227	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA ,	02/2016	1,244.75 1,245.00	1,244.75	357.60	02/2019 -	-	-	0/0
1228	TALGAON TO KALMATH - [N24001136]MoRTH,MAHARASHTRA ,	10/2016	904.70 905.00	904.70	604.05	03/2020 -	03/2020	0(O) -	2/4
1229	KALMATH TO ZARAP - [N24001137]MoRTH,MAHARASHTRA ,	09/2016	1,338.13 1,338.00	1,338.13	959.51	03/2020 -	03/2020	0(O) -	3/5
1230	PARLI PIMPLA DAHIGUDA - [N24001138]MoRTH,MAHARASHTRA ,	02/2017	205.72 205.72	205.72	30.42	06/2019 -	06/2020	12(O) -	1/4
1231	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA ,	02/2018	355.99 355.99	355.99	175.97	12/2019 -	12/2019	-	0/0
1232	WARDHA TO ARVI - [N24001150]MoRTH,MAHARASHTRA ,	02/2018	313.58 313.58	313.58	32.96	04/2020 -	04/2020	0(O) -	0/4
1233	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL,MANIPUR ,	08/2017	517.57 -	457.77	137.04	10/2018 -	10/2021	36(O) -	1/4
1234	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. - [N24001174]MoRTH,MANIPUR ,	10/2016	235.31 -	235.31	97.25	11/2020 -	11/2020	0(O) -	0/0
1235	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA ,	12/2015	479.20 -	479.20	712.89	05/2018 03/2018	10/2019	-	0/0
1236	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA ,	04/2017	553.51 -	553.51	44.39	- -	09/2021	- -	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1237	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA ,	03/2019	306.28 -	306.28	53.09	05/2019 -	-	-	0/4
1238	WIDENING TO 2 LANE RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]MoRTH,MIZORAM , ITEM RATE	11/2010	624.41 -	992.67	886.01	03/2011 12/2020	12/2020	117(O) 0	0/0
1239	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]MoRTH,MIZORAM , ITEM RATE	08/2010	193.69 -	327.92	258.71	10/2010 06/2021	06/2021	128(O) 0	0/0
1240	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]MoRTH,MIZORAM , ITEM RATE	08/2010	195.04 -	377.99	312.41	10/2010 12/2020	06/2020	116(O) -	0/0
1241	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM ,	04/2017	519.09 -	519.09	22.52	09/2019 -	09/2019	-	0/0
1242	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM ,	04/2017	640.07 -	640.07	.00	09/2019 -	09/2019	-	0/0
1243	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM ,	04/2017	642.96 -	642.96	.00	09/2019 -	09/2019	-	0/0
1244	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM ,	04/2017	473.18 -	473.18	.00	09/2019 -	09/2019	-	0/0
1245	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM ,	04/2017	537.82 -	537.82	.00	09/2019 -	09/2019	-	0/0
1246	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM ,	04/2017	518.53 -	518.53	.00	09/2019 -	09/2019	-	0/0
1247	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM ,	04/2017	404.29 -	404.29	.00	09/2019 -	09/2019	-	0/0
1248	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM ,	04/2017	428.11 -	428.11	.00	09/2019 -	09/2019	-	0/0
1249	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]MoRTH,MIZORAM ,	08/2010	186.96 -	305.61	279.13	09/2014 06/2020	06/2020	69(O) 0	0/0
1250	GWALIOR-JHANSI NH-75 - [N24000089]NHAI,MULTI STATE , PPP (ANNUITY)	12/2003	604.00 364.59	364.59	237.64	12/2009 08/2020	03/2020	123(O) 0	0/0
1251	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE , PPP (BOT)	02/2009	1,693.75 2,848.49	1,693.75	2,848.49	08/2011 -	-	-	2/2

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1252	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE , PPP (ANNUITY)	02/2011	2,498.76 -	2,498.76	2,531.46	08/2014 -	-	-	0/0
1253	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE , PPP (BOT)	09/2011	2,848.00 -	2,848.00	1,159.10	03/2014 04/2017	06/2020	75(O) 0	0/0
1254	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE , PPP (BOT)	09/2011	754.00 -	754.00	1,364.18	03/2013 11/2019	11/2020	92(O) 0	0/0
1255	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE , PPP (BOT)	10/2012	1,928.22 -	2,945.00	2,467.00	04/2015 01/2017	06/2020	62(O) 0	0/4
1256	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE ,	09/2016	1,244.10 -	1,244.10	1,445.00	- -	02/2020	- -	0/0
1257	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE ,	03/2018	1,294.47 -	1,296.00	.00	- -	-	-	0/0
1258	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE ,	03/2018	998.70 -	962.00	.00	- -	-	-	0/0
1259	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD MON-TAMLU-MERANGKONG ROAD PHEK- PFUTSERO ROA - [N24000315]MoRTH,NAGALAND , ITEM RATE	12/2010	1,296.00 -	1,296.00	.00	02/2011 -	-	-	0/0
1260	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND ,	03/2016	373.07 387.00	387.00	216.07	08/2016 -	03/2020	43(O) -	2/4
1261	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND ,	03/2016	396.52 339.55	339.55	237.99	08/2016 -	06/2020	46(O) -	2/4
1262	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND ,	03/2016	429.52 340.00	340.00	189.88	08/2016 -	03/2020	43(O) -	2/4
1263	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND ,	02/2017	507.68 -	507.68	129.13	04/2017 -	-	-	1/4
1264	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND ,	02/2017	387.00 -	387.00	145.18	09/2018 -	08/2020	23(O) -	1/4
1265	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND ,	03/2018	500.09 336.49	336.49	.00	09/2018 -	-	-	0/0
1266	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND ,	03/2018	339.57 233.35	233.35	10.15	09/2018 07/2019	-	-	0/0
1267	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND ,	03/2018	239.30 174.70	174.70	9.17	09/2018 05/2019	-	-	0/4
1268	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND ,	03/2018	285.68 -	285.68	9.58	09/2018 -	-	-	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1269	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND ,	03/2018	315.03 -	315.03	18.60	09/2018 -	-	-	0/4
1270	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND ,	03/2018	240.64 -	240.64	25.98	09/2018 -	-	-	0/4
1271	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND ,	03/2018	237.72 136.73	237.72	45.85	09/2018 11/2018	-	-	1/2
1272	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND ,	03/2018	251.97 160.10	251.97	18.67	09/2018 11/2018	-	-	0/2
1273	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND ,	03/2018	282.98 192.60	192.60	24.57	09/2018 11/2018	-	-	0/2
1274	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND ,	03/2018	215.12 -	215.12	29.88	09/2018 -	-	-	1/4
1275	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND ,	03/2018	215.79 -	215.79	16.54	09/2018 -	-	-	1/4
1276	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND ,	03/2018	272.89 -	272.89	.00	09/2018 -	-	-	0/4
1277	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND ,	03/2018	323.98 -	323.98	.00	09/2018 -	-	-	0/4
1278	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]MoRTH,NAGALAND ,	10/2016	167.62 -	167.62	61.37	12/2020 -	12/2020	0(O) -	0/0
1279	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]MoRTH,NAGALAND ,	10/2016	172.63 -	172.63	77.30	12/2020 -	12/2020	0(O) -	0/0
1280	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND ,	11/2016	336.25 -	336.25	62.64	09/2019 -	-	-	0/0
1281	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]MoRTH,NAGALAND ,	03/2017	217.35 -	217.35	35.10	11/2020 -	11/2020	0(O) -	0/0
1282	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180]MoRTH,NAGALAND ,	03/2019	237.51 -	237.51	.00	12/2022 -	12/2022	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1283	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA , PPP (BOT)	03/2012	1,410.00 -	1,410.00	1,935.14	09/2014 -	-	-	0/0
1284	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA , PPP (BOT)	12/2011	1,047.00 -	1,047.00	1,874.43	06/2014 -	03/2019	-	0/0
1285	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MoRTH,ODISHA , EPC	01/1991	218.63 -	218.63	29.27	10/2017 -	-	-	0/0
1286	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MoRTH,ODISHA ,	01/1991	229.41 -	229.41	6.65	05/2018 -	-	-	0/0
1287	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]MoRTH,ODISHA , EPC	07/2014	342.05 -	342.05	258.91	01/2017 -	-	-	0/0
1288	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA ,	07/2015	1,282.94 -	1,282.94	288.42	- -	03/2021	- -	0/0
1289	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA ,	12/2015	752.28 -	752.28	76.78	- -	-	-	0/1
1290	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]MoRTH,ODISHA , EPC	12/2011	159.39 -	159.39	210.29	11/2017 -	-	-	0/0
1291	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH,ODISHA , EPC	12/2011	191.08 -	191.08	99.98	08/2015 -	-	-	0/0
1292	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA ,	02/2016	1,069.65 -	1,069.65	546.51	- -	03/2020	- -	0/0
1293	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA ,	09/2016	2,510.04 -	2,510.04	358.51	08/2019 -	03/2021	19(O) -	0/0
1294	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA ,	10/2016	1,008.96 -	1,008.96	595.10	- -	03/2021	- -	0/0
1295	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH,ODISHA ,	03/2014	191.50 192.00	192.00	136.19	05/2016 -	-	-	0/0
1296	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MoRTH,ODISHA ,	01/2015	326.63 327.00	326.63	249.26	04/2018 -	-	-	0/0
1297	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MoRTH,ODISHA ,	02/2015	239.91 240.00	160.00	147.25	10/2017 -	-	-	0/0
1298	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MoRTH,ODISHA ,	07/2014	342.05 342.00	342.00	258.91	01/2017 -	-	-	0/0
1299	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH,ODISHA ,	08/2013	171.96 172.00	172.00	88.30	06/2016 -	-	-	0/0
1300	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MoRTH,ODISHA ,	06/2016	157.30 157.00	157.30	97.29	06/2018 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1301	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA ,	03/2017	1,288.07 -	1,420.00	532.31	03/2020 -	03/2021	12(O) -	0/0
1302	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA , Central Sector Projects	07/2017	476.56 -	476.56	1.49	07/2017 11/2020	06/2021	47(O) 0	0/0
1303	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA ,	12/2017	686.65 -	686.65	114.36	- 07/2020	06/2021	- 0	0/0
1304	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA ,	12/2017	417.51 -	417.51	44.14	- -	06/2021	- -	0/0
1305	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA ,	01/2018	953.09 -	953.09	224.11	- 05/2020	06/2021	- 0	0/0
1306	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA ,	01/2018	668.86 -	668.86	175.29	- 05/2020	06/2021	- 0	0/0
1307	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA ,	01/2018	633.68 -	633.68	.00	- -	-	-	0/0
1308	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA ,	01/2018	614.48 -	614.48	93.00	- -	08/2021	- -	0/0
1309	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA ,	01/2018	564.66 -	564.66	89.77	- -	08/2021	- -	0/0
1310	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA ,	01/2018	686.65 -	686.65	105.69	- 03/2020	06/2021	- 0	0/0
1311	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK - [N24000737]NHAI,ODISHA ,	01/2018	1,522.00 -	1,522.00	243.52	- 06/2021	06/2021	- 0	0/0
1312	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA ,	01/2018	999.00 -	999.00	.00	- -	06/2021	- -	0/0
1313	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA ,	01/2018	503.88 -	503.88	8.84	- -	06/2021	- -	0/0
1314	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA , EPC	03/2018	806.11 -	806.11	21.39	- -	04/2021	- -	0/0
1315	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26. - [N24000911]MoRTH,ODISHA ,	03/2016	165.06 -	165.06	92.59	12/2016 -	-	-	0/0
1316	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MoRTH,ODISHA ,	08/2016	287.70 -	287.70	153.90	02/2017 -	-	-	0/0
1317	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH,ODISHA ,	09/2016	295.67 -	295.67	127.75	02/2017 -	-	-	0/0
1318	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH,ODISHA ,	12/2016	223.50 -	223.50	44.52	08/2018 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1319	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH,ODISHA ,	12/2016	206.88 -	206.88	41.69	04/2018 -	-	-	0/0
1320	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH,ODISHA ,	03/2018	214.23 -	214.23	23.44	08/2018 -	-	-	0/0
1321	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH,ODISHA ,	03/2018	199.16 -	199.16	25.63	08/2018 -	-	-	0/0
1322	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]MoRTH,PUNJAB , EPC	12/2015	766.36 -	766.36	685.36	- 09/2019	-	-	0/0
1323	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]MoRTH,PUNJAB , EPC	11/2015	847.02 -	847.02	795.00	- 12/2019	-	-	0/0
1324	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]MoRTH,PUNJAB , EPC	11/2015	889.24 904.82	904.82	739.41	- 05/2020	-	-	0/0
1325	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB ,	09/2014	479.00 -	479.00	453.80	- -	06/2020	- -	0/0
1326	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB ,	10/2015	447.29 746.43	746.43	614.07	12/2017 06/2020	06/2020	30(O) 6	0/0
1327	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]MoRTH,PUNJAB , EPC	06/2015	892.17 -	892.17	648.44	- 02/2018	-	-	0/0
1328	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB ,	08/2016	1,388.34 2,541.32	2,587.50	1,449.00	09/2019 03/2020	03/2020	6(O) 6	0/0
1329	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB ,	08/2016	1,169.61 1,367.00	1,169.61	1,203.12	- -	04/2020	- -	0/0
1330	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB ,	03/2017	754.54 -	756.27	193.96	03/2020 -	08/2021	17(O) -	0/0
1331	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB ,	02/2018	261.76 -	207.00	112.77	- -	01/2021	- -	0/0
1332	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB , EPC	03/2018	199.90 149.90	199.90	112.43	- -	-	-	0/0
1333	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB , EPC	03/2018	196.05 149.90	196.05	143.03	- -	01/2020	- -	0/0
1334	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905]MoRTH,PUNJAB ,	03/2018	322.48 -	322.48	153.18	07/2020 -	07/2020	0(O) -	0/0
1335	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906]MoRTH,PUNJAB ,	03/2018	173.24 -	173.24	56.66	06/2020 -	06/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1336	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]MoRTH,PUNJAB ,	03/2018	293.10 -	293.10	63.14	08/2020 -	08/2020	0(O) -	0/0
1337	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH,PUNJAB ,	10/2017	1,069.59 -	1,069.59	663.50	10/2019 12/2020	12/2020	14(O) 14	0/0
1338	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH,PUNJAB ,	03/2018	170.57 192.48	170.57	8.14	11/2020 -	05/2021	6(O) -	0/0
1339	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927]MoRTH,PUNJAB ,	03/2018	293.64 -	293.64	28.24	08/2020 -	08/2020	0(O) -	0/0
1340	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]MoRTH,PUNJAB ,	03/2018	293.64 -	293.64	134.32	08/2020 -	08/2020	0(O) -	0/0
1341	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MoRTH,RAJASTHAN , EPC	10/2014	269.22 -	269.22	33.24	01/2015 -	-	-	0/0
1342	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MoRTH,RAJASTHAN , EPC	10/2014	257.09 -	257.09	14.18	01/2015 -	-	-	0/0
1343	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MoRTH,RAJASTHAN , EPC	10/2013	278.87 -	278.87	.00	05/2014 -	-	-	0/0
1344	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MoRTH,RAJASTHAN , ITEM RATE	01/1991	376.52 -	376.52	.00	04/2014 -	-	-	0/0
1345	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MoRTH,RAJASTHAN , EPC	02/2015	383.40 -	383.40	244.68	03/2015 -	-	-	0/0
1346	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MoRTH,RAJASTHAN , EPC	12/2015	621.43 -	621.43	387.22	06/2018 -	-	-	0/4
1347	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN ,	09/2014	425.19 -	425.19	276.40	09/2016 09/2014	10/2019	-	0/0
1348	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN ,	10/2015	597.00 -	597.00	587.64	10/2017 -	03/2020	29(O) -	3/4
1349	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN , PPP (BOT)	11/2012	530.07 -	530.07	556.02	08/2016 -	06/2020	46(O) -	0/0
1350	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN , PPP (BOT)	08/2014	822.90 -	822.90	844.08	04/2018 -	-	-	0/0
1351	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]MoRTH,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	2,323.04	10/2013 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1352	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]MORTH,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	492.00	10/2013 -	-	-	0/4
1353	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN , PPP (BOT)	02/2008	1,673.70 -	1,673.70	3,326.93	10/2011 -	-	-	0/0
1354	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN ,	08/2015	275.90 -	275.90	289.13	- 02/2016	10/2019	-	0/0
1355	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI,RAJASTHAN , PPP (BOT)	06/2016	637.18 -	637.18	550.35	06/2019 -	09/2019	-	0/0
1356	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN , PPP (BOT)	06/2016	763.23 -	763.23	439.88	06/2019 -	11/2019	-	1/1
1357	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589]NHAI,RAJASTHAN ,	06/2016	649.00 -	649.00	322.84	06/2019 -	09/2019	-	0/0
1358	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN ,	07/2016	688.70 881.00	688.70	870.48	- 05/2017	02/2020	- 1	0/0
1359	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN ,	07/2016	331.46 -	331.46	267.94	10/2018 -	-	-	0/0
1360	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN ,	08/2016	320.30 -	320.30	237.81	01/2019 -	-	-	4/4
1361	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN ,	09/2016	1,239.82 -	1,239.82	1,427.14	- -	05/2020	- -	3/4
1362	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN ,	09/2016	1,100.19 -	1,145.31	1,045.00	- -	05/2020	- -	0/0
1363	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN ,	12/2016	1,031.95 -	1,031.95	367.00	- -	08/2020	- -	0/0
1364	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN ,	04/2017	894.00 -	929.32	760.00	04/2020 -	04/2020	0(O) -	0/0
1365	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN , Central Sector Projects	10/2017	964.17 -	964.17	390.91	10/2017 -	11/2020	37(O) -	0/0
1366	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN ,	12/2017	1,308.73 -	1,308.73	99.68	- -	12/2020	- -	0/0
1367	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN ,	02/2018	1,103.88 -	1,103.88	404.43	- -	09/2020	- -	0/0
1368	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN ,	02/2018	741.86 -	741.86	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1369	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN ,	02/2018	716.76 -	716.76	283.46	- -	-	-	0/0
1370	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN ,	03/2018	874.25 -	874.25	288.37	- -	-	-	0/0
1371	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN ,	03/2018	1,158.35 -	1,158.35	496.04	- -	-	-	0/0
1372	WIDENING STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950]MoRTH,RAJASTHAN ,	11/2017	187.82 -	187.82	95.15	04/2018 -	-	-	2/4
1373	NETRA VILLAGE TO MANDORE SECTION OF NH-65 KM 267+500 TO 296+070 (4L) UNDER EPC. - [N24000951]MoRTH,RAJASTHAN ,	10/2014	382.81 -	382.81	335.93	01/2015 -	-	-	4/4
1374	UP-GRADATION TO TWO LANE WITH PAVED SHOULDER FOR SECTION FROM KM 58.000 TO KM 91.600 (BALOTRA TO SAN - [N24000952]MoRTH,RAJASTHAN ,	01/2017	179.32 -	179.32	120.78	11/2017 -	-	-	3/4
1375	CONSTRUCTION OF NAGAU BYPASS FROM EXISTING KM 166/260 TO KM 180/500 OF NH-65 ON EPC MODE. - [N24000953]MoRTH,RAJASTHAN ,	03/2016	155.77 -	155.77	110.34	09/2016 -	-	-	3/4
1376	NAGAU-BIKANER OF NH-11 (2L+PS) UNDER PPP. - [N24000954]MoRTH,RAJASTHAN ,	01/2012	378.07 478.73	478.73	188.98	01/2014 -	-	-	1/4
1377	CITTORGARH-NEEMACH (4L) OF NH-79 AND NIMBAHARA PRATAPGARH (2L+PS) OF NH-113 UNDER PPP. - [N24000955]MoRTH,RAJASTHAN ,	10/2012	511.21 -	511.21	814.79	10/2013 -	-	-	3/4
1378	DEVELOPMENT AND OPERATION OF BIKANER-SURATGARH SECTION OF NH-15 BY 2L+PS IN THE STATE OF RAJASTHAN - [N24000956]MoRTH,RAJASTHAN ,	03/2009	501.00 671.54	671.54	659.98	09/2013 -	-	-	3/4
1379	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709 - [N24000957]MoRTH,RAJASTHAN ,	11/2017	163.95 -	163.95	128.05	04/2018 -	-	-	3/4
1380	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000958]MoRTH,RAJASTHAN ,	02/2018	370.30 -	370.30	207.58	06/2018 -	-	-	1/4
1381	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000959]MoRTH,RAJASTHAN ,	02/2018	341.79 -	341.79	299.48	05/2018 -	-	-	1/4
1382	CONSTRUCTION OF 4 LANING BY CC PAVEMENT ON KOTA-DARAH OF NH-12 FROM 256/550 TO 289/550 UNDER EPC. - [N24000960]MoRTH,RAJASTHAN ,	12/2015	621.43 -	621.43	427.45	10/2016 -	-	-	3/4
1383	UP-GRADATION TO 2 LANE WITH PAVED SHOULDER FOR SECTION FROM KM 118.900 TO KM 156.955 BALOTRA TOSANDE - [N24000961]MoRTH,RAJASTHAN ,	01/2017	163.54 -	163.54	106.25	07/2017 -	-	-	2/4
1384	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MoRTH,RAJASTHAN ,	03/2019	178.13 -	178.13	25.21	- -	-	-	0/0
1385	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]MoRTH,SIKKIM ,	04/2013	151.59 240.58	151.59	196.76	08/2013 -	12/2019	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1386	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]MoRTH,SIKKIM , ITEM RATE	04/2013	166.27 -	166.27	141.31	08/2013 -	-	-	0/0
1387	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]MoRTH,SIKKIM , ITEM RATE	01/2013	182.28 -	269.14	185.49	02/2013 -	12/2019	-	0/0
1388	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM , Central Sector Projects	04/2017	388.00 -	447.37	155.85	10/2017 -	-	-	2/4
1389	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA - [N24000766]NHIDCL,SIKKIM ,	04/2017	318.42 -	318.42	66.63	11/2017 -	-	-	2/4
1390	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM ,	03/2017	375.80 -	375.80	77.39	- -	-	-	0/0
1391	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM ,	11/2017	290.05 -	290.05	54.13	11/2017 -	-	-	1/4
1392	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM ,	03/2018	264.84 -	264.84	.00	06/2018 -	-	-	0/4
1393	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU , PPP (BOT)	09/2011	1,250.00 -	1,250.00	1,336.07	12/2013 -	06/2020	78(O) -	0/0
1394	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU ,	06/2011	600.00 -	600.00	329.92	06/2013 01/2019	08/2020	86(O) 0	0/0
1395	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU , PPP (ANNUITY)	05/2010	374.00 -	374.00	237.00	05/2013 -	-	-	0/0
1396	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU , PPP (ANNUITY)	09/2011	485.00 -	485.00	406.68	08/2013 -	-	-	0/0
1397	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU , PPP (ANNUITY)	04/2012	624.00 -	624.00	350.79	04/2014 -	-	-	0/0
1398	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MoRTH,TAMIL NADU , EPC	03/2015	258.97 -	268.92	.00	08/2015 -	-	-	0/0
1399	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MoRTH,TAMIL NADU , EPC	03/2015	157.18 162.00	162.00	.00	07/2015 -	-	-	0/0
1400	CONSTRUCTION OF PAVED SHOULDERS INCULGING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MoRTH,TAMIL NADU , EPC	11/2015	154.14 -	154.14	.00	08/2015 -	-	-	0/0
1401	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU ,	05/2015	1,387.11 -	1,387.11	980.46	11/2017 -	07/2019	-	0/0
1402	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU ,	06/2015	563.92 -	563.92	93.53	12/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1403	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU ,	07/2014	401.11 -	401.11	273.89	01/2017 -	-	-	0/0
1404	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU , PPP (BOT)	03/2007	516.00 -	516.00	886.96	07/2008 -	-	-	0/0
1405	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU ,	02/2016	707.82 -	707.82	381.40	08/2018 -	03/2020	19(O) -	0/0
1406	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU ,	02/2016	641.17 -	641.17	370.82	07/2018 -	05/2020	22(O) -	0/0
1407	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU ,	03/2017	848.45 -	848.45	103.14	03/2020 -	03/2020	0(O) -	0/0
1408	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU , Central Sector Projects	03/2016	641.17 -	641.17	370.82	07/2016 -	05/2020	46(O) -	0/0
1409	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU , Central Sector Projects	08/2017	1,176.37 -	1,176.37	207.17	08/2017 -	09/2020	37(O) -	0/0
1410	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU , Central Sector Projects	09/2017	244.27 -	244.27	177.41	09/2017 -	04/2020	31(O) -	0/0
1411	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU , Central Sector Projects	09/2017	1,227.87 -	1,227.87	387.40	09/2017 -	08/2020	35(O) -	0/0
1412	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU ,	12/2017	379.90 -	379.90	125.68	-	03/2020	-	0/0
1413	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU ,	02/2018	1,166.26 -	1,166.26	163.29	-	02/2021	-	0/0
1414	FOUR LANING OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULAM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU , EPC	03/2018	505.35 -	505.35	100.44	-	11/2020	-	0/0
1415	FOUR LANING OF MADURAI- CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTIKULAM (7/300) - [N24000827]NHAI,TAMIL NADU , EPC	03/2018	628.71 -	628.71	120.55	-	11/2020	-	0/0
1416	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU ,	03/2018	633.55 -	482.04	.00	-	-	-	0/0
1417	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU ,	03/2018	1,016.92 -	1,071.00	.00	-	04/2021	-	0/0
1418	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU ,	03/2018	2,065.96 -	2,169.00	.00	-	-	-	0/0
1419	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA , PPP (BOT)	04/2014	1,266.60 -	1,544.00	1,446.45	09/2016 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1420	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]MoRTH,TELANGANA , EPC	01/2014	270.00 -	270.00	19.84	03/2016 -	-	-	1/4
1421	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA , EPC	03/2015	153.21 -	153.21	100.10	01/2017 -	-	-	0/0
1422	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA ,	12/2015	1,423.96 897.03	897.03	796.56	11/2018 07/2019	06/2020	19(O) 3	0/0
1423	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA ,	03/2017	4,429.00 -	4,429.00	.00	03/2017 -	-	-	0/0
1424	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K - [N24000804]NHAI,TELANGANA ,	03/2018	802.65 -	802.65	91.76	- -	-	-	0/0
1425	FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA ,	03/2018	950.63 -	950.63	283.36	- -	-	-	0/0
1426	FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA ,	03/2018	857.62 -	857.62	4.89	- -	-	-	0/0
1427	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI,TELANGANA ,	03/2018	828.29 998.89	828.29	.00	- 11/2019	-	-	0/0
1428	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA ,	10/2016	298.32 -	298.32	83.57	02/2019 -	06/2020	16(O) -	0/0
1429	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA ,	10/2016	248.83 -	248.83	91.52	03/2019 -	03/2020	12(O) -	0/0
1430	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH,TELANGANA ,	01/2017	244.54 -	244.54	138.52	05/2019 -	-	-	0/0
1431	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]MoRTH,TELANGANA ,	01/2017	196.52 -	196.52	103.22	10/2019 -	-	-	0/0
1432	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]MoRTH,TELANGANA ,	01/2017	283.00 -	283.00	166.22	12/2019 -	-	-	0/0
1433	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]MoRTH,TELANGANA ,	01/2017	359.27 -	359.27	237.90	05/2019 -	-	-	0/0
1434	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH,TELANGANA ,	01/2017	300.00 -	300.00	100.33	05/2019 -	03/2020	10(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1435	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]MoRTH,TELANGANA ,	01/2018	283.15 -	283.15	42.22	05/2020 -	05/2020	0(O) -	0/0
1436	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]MoRTH,TELANGANA ,	01/2018	230.03 -	230.03	127.98	12/2019 -	-	-	0/0
1437	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]MoRTH,TELANGANA ,	02/2018	206.13 -	206.13	127.86	06/2020 -	06/2020	0(O) -	0/0
1438	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH,TELANGANA ,	02/2018	294.13 -	294.13	39.44	11/2019 -	-	-	0/0
1439	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH,TELANGANA ,	02/2018	220.28 -	220.28	37.58	11/2019 -	-	-	0/0
1440	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]MoRTH,TELANGANA ,	02/2018	426.52 -	426.52	225.51	04/2020 -	04/2020	0(O) -	0/0
1441	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]MoRTH,TELANGANA ,	03/2018	322.81 -	322.81	1.66	09/2020 -	09/2020	0(O) -	0/0
1442	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]MoRTH,TELANGANA ,	03/2018	626.76 -	626.76	80.66	07/2020 -	07/2020	0(O) -	0/0
1443	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH,TELANGANA ,	01/2017	605.08 -	605.08	273.88	10/2019 -	-	-	0/0
1444	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH,TELANGANA ,	03/2018	192.67 -	192.67	107.37	07/2019 -	-	-	0/0
1445	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH,TELANGANA ,	01/2019	193.19 -	193.19	.00	- -	-	-	0/0
1446	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA , EPC	10/2014	369.00 -	369.00	319.05	03/2018 12/2019	-	-	3/4
1447	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]MoRTH,TRIPURA ,	10/2016	171.90 -	171.90	23.19	08/2020 -	08/2020	0(O) -	0/0
1448	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH , PPP (BOT)	02/2011	1,141.00 -	1,141.00	1,715.42	08/2013 -	-	-	0/0
1449	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH , PPP (BOT)	03/2011	1,046.00 -	1,046.00	805.19	09/2013 -	-	-	0/0
1450	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH , PPP (BOT)	07/2012	291.36 -	291.36	459.07	01/2014 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1451	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH , PPP (BOT)	03/2013	1,573.00 -	1,573.00	2,078.25	09/2015 -	-	-	0/0
1452	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MoRTH,UTTAR PRADESH , EPC	01/2014	282.41 -	282.41	155.53	03/2016 -	-	-	0/0
1453	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH ,	05/2015	261.09 275.00	261.09	240.96	05/2017 -	-	-	0/0
1454	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH ,	04/2014	351.34 -	351.34	433.68	01/2016 -	-	-	0/0
1455	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH ,	09/2015	368.73 -	368.73	239.04	09/2016 03/2018	03/2018	-	0/0
1456	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH ,	06/2014	301.04 -	301.04	207.94	01/2016 -	-	-	0/0
1457	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI,UTTAR PRADESH ,	04/2014	495.78 -	495.78	633.24	01/2016 -	-	-	0/0
1458	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]MoRTH,UTTAR PRADESH , EPC	10/2013	445.89 -	653.29	464.05	03/2017 -	-	-	0/0
1459	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]MoRTH,UTTAR PRADESH , ITEM RATE	11/2010	305.49 -	305.49	131.08	03/2017 -	-	-	0/0
1460	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH , PPP (BOT)	07/2015	1,657.20 -	1,657.20	2,345.00	01/2019 -	-	-	0/0
1461	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH ,	12/2015	611.65 -	611.65	728.24	06/2016 -	-	-	0/0
1462	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH ,	01/2016	815.28 2,182.03	815.28	520.89	06/2018 -	06/2020	24(O) -	0/0
1463	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH ,	01/2016	1,027.53 2,433.38	1,027.53	601.13	06/2018 -	06/2020	24(O) -	0/0
1464	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH ,	06/2016	667.00 2,257.49	667.00	464.05	07/2018 -	04/2020	21(O) -	0/0
1465	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH ,	12/2015	667.00 3,007.86	667.00	549.07	06/2018 -	04/2020	22(O) -	0/0
1466	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH,UTTAR PRADESH , EPC	05/2013	164.54 -	164.54	126.41	08/2015 -	12/2019	-	0/0
1467	MEERUT-BULANDSHAHAR - [N24000539]NHAI,UTTAR PRADESH ,	01/2016	683.24 868.77	987.94	727.69	- 10/2019	02/2020	- 0	0/2
1468	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH ,	01/2016	1,081.57 -	1,057.60	1,041.85	06/2019 12/2016	09/2019	-	0/0
1469	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH ,	03/2016	676.73 -	676.73	945.17	04/2019 -	-	-	0/0
1470	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH ,	03/2016	1,404.50 3,267.94	1,404.50	2,977.58	- 03/2017	-	-	0/0
1471	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH ,	03/2016	1,396.74 -	1,396.74	227.26	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1472	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH ,	03/2016	1,587.49 -	2,982.00	276.87	04/2019 -	-	-	0/0
1473	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH ,	03/2016	899.00 -	899.00	641.51	04/2019 07/2020	07/2020	15(O) 0	0/0
1474	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH ,	03/2016	1,668.00 -	1,668.00	946.08	- -	01/2020	- -	0/0
1475	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH ,	03/2016	1,408.00 -	1,408.00	442.70	- -	07/2020	- -	0/0
1476	4-LANNING OF NAGINA-KSHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH ,	03/2016	1,737.00 -	1,737.00	1,159.07	- -	04/2020	- -	0/0
1477	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH ,	08/2016	2,016.00 -	2,016.00	1,996.00	04/2019 -	11/2019	-	0/0
1478	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH ,	12/2016	534.55 -	531.00	433.62	- -	09/2019	-	0/0
1479	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH ,	01/2017	450.68 -	450.68	397.62	- -	-	-	0/0
1480	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH ,	03/2017	1,373.28 -	1,373.28	571.96	03/2020 -	11/2020	8(O) -	0/4
1481	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH ,	03/2017	1,184.71 -	1,310.00	563.15	03/2020 -	08/2020	5(O) -	0/4
1482	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH ,	03/2017	1,989.00 2,602.09	1,989.00	892.35	03/2020 11/2017	05/2020	2(O) 0	0/0
1483	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH ,	03/2017	2,064.99 -	2,447.00	2,029.34	03/2020 06/2020	06/2020	3(O) 0	0/0
1484	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH ,	12/2017	1,232.21 3,207.63	1,087.00	562.94	- 02/2018	05/2020	- 0	0/0
1485	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH ,	12/2017	207.00 -	207.00	34.77	- 03/2020	12/2020	- 0	0/0
1486	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH ,	12/2017	305.00 -	305.00	.00	- -	-	-	0/0
1487	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH ,	01/2018	450.77 929.89	450.77	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1488	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH ,	02/2018	670.50 -	670.50	44.24	- -	-	-	0/0
1489	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH ,	03/2018	809.07 1,065.70	809.07	176.96	- -	-	-	0/0
1490	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH ,	03/2018	925.40 1,197.00	1,197.00	563.83	- -	-	-	0/0
1491	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH ,	03/2018	1,117.84 -	1,117.84	.00	- -	12/2021	-	0/0
1492	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH ,	03/2018	2,140.93 -	2,140.93	1,230.96	- -	-	-	0/0
1493	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH ,	03/2018	1,120.57 1,332.00	1,332.00	510.96	- -	-	-	0/0
1494	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH ,	03/2018	1,025.80 -	677.07	203.25	- -	-	-	0/0
1495	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH ,	03/2018	1,115.28 -	770.04	288.52	- -	-	-	0/0
1496	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH ,	02/2018	972.77 1,444.25	972.77	494.71	- 02/2019	-	-	0/0
1497	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH ,	11/2016	326.99 327.00	326.99	4.03	- -	-	-	0/0
1498	REHABILITATION AND UPGRADATION OF HARPALPUR -SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942]MoRTH,UTTAR PRADESH ,	03/2016	208.50 -	208.50	141.54	11/2019 -	03/2020	4(O) -	0/0
1499	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA - [N24001139]MoRTH,UTTAR PRADESH ,	10/2016	218.94 219.00	218.94	120.69	03/2020 -	03/2020	0(O) -	0/0
1500	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]MoRTH,UTTAR PRADESH ,	11/2016	215.16 215.00	215.16	160.61	09/2019 -	10/2019	-	0/0
1501	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH,UTTAR PRADESH ,	03/2016	240.30 240.00	240.30	198.06	01/2020 -	03/2020	2(O) -	0/0
1502	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO - [N24001143]MoRTH,UTTAR PRADESH ,	10/2016	176.94 177.00	176.94	141.11	10/2018 -	09/2019	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1503	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]MoRTH,UTTAR PRADESH ,	10/2013	445.89 653.00	653.29	469.64	03/2017 -	10/2019	-	0/0
1504	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH - [N24001145]MoRTH,UTTAR PRADESH ,	05/2013	164.54 165.00	164.54	127.34	08/2015 -	03/2020	55(O) -	0/0
1505	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]MoRTH,UTTAR PRADESH ,	03/2016	249.50 -	249.50	160.60	05/2019 -	03/2020	10(O) -	0/0
1506	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2- - [N24001147]MoRTH,UTTAR PRADESH ,	10/2016	239.63 -	239.63	212.53	02/2019 -	07/2019	-	0/0
1507	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148]MoRTH,UTTAR PRADESH ,	03/2016	599.34 -	599.34	492.15	01/2020 -	01/2020	0(O) -	0/0
1508	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH – 14 - [N24001185]NHAI,UTTAR PRADESH , PPP BOT (Hybrid Annuity)	11/2017	2,159.00 -	2,159.00	867.86	01/2019 -	-	-	0/0
1509	REHABILITATION AND UPGRADATION OF BARAICH - SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA - [N24001202]MoRTH,UTTAR PRADESH ,	03/2016	388.83 -	388.83	304.70	12/2019 -	12/2019	-	0/0
1510	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203]MoRTH,UTTAR PRADESH ,	10/2016	218.90 -	218.90	64.59	03/2020 -	03/2020	0(O) -	0/0
1511	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]MoRTH,UTTAR PRADESH ,	07/2016	208.88 -	208.88	95.59	10/2019 -	06/2020	8(O) -	0/0
1512	R AND U FROM KM 385.00 TO KM 420.000 TO 2-LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404 - [N24001205]MoRTH,UTTAR PRADESH ,	12/2016	209.10 -	209.10	160.28	10/2019 04/2020	04/2020	6(O) 0	0/0
1513	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]MoRTH,UTTAR PRADESH ,	03/2018	263.89 242.05	242.05	139.94	04/2020 -	04/2020	0(O) -	0/0
1514	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]MoRTH,UTTAR PRADESH ,	03/2018	185.18 -	185.18	79.93	02/2020 -	02/2020	0(O) -	0/0
1515	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208]MoRTH,UTTAR PRADESH ,	03/2018	288.30 -	288.30	41.74	08/2020 -	08/2020	0(O) -	0/0
1516	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]MoRTH,UTTAR PRADESH ,	03/2016	296.50 -	296.50	74.77	09/2020 -	09/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1517	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH,UTTAR PRADESH ,	03/2018	306.59 -	306.59	.00	- -	-	-	0/0
1518	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH,UTTAR PRADESH ,	11/2018	281.45 -	281.45	.00	- -	-	-	0/0
1519	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 KM - [N24001230]MoRTH,UTTAR PRADESH ,	11/2018	281.45 -	281.45	2.36	12/2020 -	12/2020	0(O) -	0/0
1520	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND ,	11/2011	478.51 -	478.00	315.11	10/2013 -	08/2020	82(O) -	0/0
1521	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND ,	03/2016	720.00 -	720.00	343.72	- 10/2020	10/2020	- 0	0/0
1522	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND ,	03/2016	1,443.00 -	1,443.00	1,246.85	- -	02/2020	- -	0/0
1523	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND ,	11/2012	605.84 -	722.46	722.46	07/2018 12/2019	02/2020	19(O) 0	0/0
1524	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND ,	03/2018	274.31 -	274.31	29.13	05/2018 -	-	-	1/4
1525	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND ,	03/2018	403.36 -	403.36	99.65	06/2018 -	-	-	1/4
1526	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND ,	03/2018	417.24 -	417.24	112.62	05/2018 -	-	-	1/4
1527	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH,UTTARAKHAND ,	12/2017	257.34 -	257.34	62.79	12/2019 -	-	-	0/0
1528	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH,UTTARAKHAND ,	12/2017	200.34 -	200.34	31.00	12/2019 -	-	-	0/0
1529	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MoRTH,UTTARAKHAND ,	12/2017	248.22 -	248.22	57.20	12/2019 -	-	-	0/0
1530	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MoRTH,UTTARAKHAND ,	06/2017	282.08 -	282.08	77.05	06/2019 -	-	-	0/0
1531	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH,UTTARAKHAND ,	11/2017	232.81 -	232.81	59.44	11/2019 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1532	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH,UTTARAKHAND ,	11/2017	283.51 -	283.51	126.38	11/2019 -	-	-	0/0
1533	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH,UTTARAKHAND ,	11/2017	266.52 -	266.52	144.27	11/2019 -	-	-	0/0
1534	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MoRTH,UTTARAKHAND ,	02/2018	418.88 -	418.88	88.00	02/2020 -	02/2020	0(O) -	0/0
1535	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MoRTH,UTTARAKHAND ,	02/2018	293.68 -	293.68	11.57	- -	-	-	0/0
1536	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MoRTH,UTTARAKHAND ,	05/2018	248.00 -	248.00	.00	05/2020 -	05/2020	0(O) -	0/0
1537	REHABILITATION AND UPGRADE OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH,UTTARAKHAND ,	03/2018	460.73 -	461.00	.00	- -	-	-	0/0
1538	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL,UTTARAKHAND ,	03/2018	1,383.78 -	1,383.78	138.75	07/2018 -	-	-	1/5
1539	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND ,	08/2016	234.88 -	208.89	118.26	12/2017 -	-	-	0/0
1540	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL , PPP (BOT)	02/2011	1,078.84 -	1,078.84	2,195.64	08/2013 -	05/2020	81(O) -	3/4
1541	4-LANING OF BRAHAMPUR-FARAKA - [N24000203]NHAI, WEST BENGAL , PPP (BOT)	02/2011	998.79 -	998.79	1,822.59	08/2013 -	03/2021	91(O) -	3/4
1542	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL , PPP (BOT)	04/2012	1,396.18 -	1,396.18	2,894.94	09/2014 -	03/2020	66(O) -	0/0
1543	REHABILITATION AND UPGRADE TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MoRTH, WEST BENGAL ,	01/1991	322.00 -	322.00	56.41	03/2018 -	-	-	0/0
1544	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL ,	10/2015	361.15 -	361.15	186.64	- -	01/2020	- -	0/0
1545	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL ,	12/2015	1,083.00 -	1,083.00	1,487.87	06/2018 -	-	-	0/0
1546	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL , PPP (BOT)	04/2014	1,665.00 -	1,665.00	4,357.89	- -	-	-	0/0
1547	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK HALDIA - [N24000553]NHAI, WEST BENGAL ,	03/2016	229.37 -	229.37	112.94	11/2018 08/2020	08/2020	21(O) 5	0/0
1548	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL ,	09/2016	767.03 767.03	767.03	601.10	08/2018 -	09/2019	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1549	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITA AND PANITNAKI I - [N24000770]NHIDCL, WEST BENGAL ,	03/2017	158.65 -	158.65	59.53	06/2018 -	-	-	0/0
1550	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI, WEST BENGAL ,	03/2018	1,261.98 -	1,261.98	793.49	- -	07/2021	-	0/0
1551	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B NH-31C NH-31 NH-10 O - [N24000871]MoRTH, WEST BENGAL ,	08/2014	600.87 720.97	720.97	659.24	11/2017 05/2019	05/2019	-	0/0
1552	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717 NH-31 NH-31C NH-317A O - [N24000873]MoRTH, WEST BENGAL ,	08/2014	823.20 937.76	937.76	751.29	11/2017 06/2019	06/2019	-	0/0
1553	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]MoRTH, WEST BENGAL ,	03/2016	271.17 291.20	291.20	110.98	11/2018 11/2019	11/2019	-	0/0
1554	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]MoRTH, WEST BENGAL ,	01/2017	396.86 396.86	396.86	185.31	09/2019 -	-	-	0/0
1555	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879]MoRTH, WEST BENGAL ,	03/2017	202.69 202.69	202.69	103.14	11/2019 -	-	-	0/0
1556	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]MoRTH, WEST BENGAL ,	02/2018	426.18 426.18	426.18	224.22	09/2020 -	-	-	0/0
1557	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]MoRTH, WEST BENGAL ,	02/2018	218.70 218.70	218.70	45.72	11/2020 -	-	-	0/0
1558	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE BAGDO) - [N24000883]MoRTH, WEST BENGAL ,	03/2018	254.30 254.30	254.30	53.46	10/2020 -	10/2020	0(O) -	0/0
1559	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND) - [N24000885]MoRTH, WEST BENGAL ,	03/2016	160.27 213.97	213.97	20.11	08/2019 -	08/2021	24(O) -	0/0
1560	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH, WEST BENGAL ,	06/2016	236.78 263.26	263.26	59.92	08/2019 -	08/2021	24(O) -	0/0
1561	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]MoRTH, WEST BENGAL ,	04/2014	279.70 398.52	398.52	322.91	08/2017 07/2019	07/2019	-	0/0
	Total		5,13,537.42 -	5,28,085.90	3,00,798.25				323/1069
	SHIPPING AND PORTS								

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1562	JAL MARG VIKAS PROJECT - [N25000072]JWAI,MULTI STATE ,	01/2018	4,200.00 5,369.18	5,369.18	1,540.69	03/2023 03/2023	03/2023	0(O) 0	0/0
	Total		4,200.00 -	5,369.18	1,540.69				0/0
	<u>TELECOMMUNICATIONS</u>								
1563	GSM-RF EXPANSION PROJECT MTNL DELHI (3G) - [N26000105]MTNL,DELHI ,	06/2016	418.26 -	418.26	367.04	06/2017 -	-	-	0/0
1564	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]BSNL,MAHARASHTRA , Central Sector Projects	01/2018	231.80 240.10	240.10	119.92	10/2018 02/2020	02/2020	16(O) 1	0/0
1565	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE ,	03/2012	13,334.00 -	24,664.00	12,146.00	07/2015 -	05/2020	58(O) -	0/0
1566	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI,MULTI STATE , Central Sector Projects	09/2014	2,111.17 -	2,011.17	253.90	09/2014 -	-	-	0/70
	Total		16,095.23 -	27,333.53	12,886.86				0/70
	<u>URBAN DEVELOPMENT</u>								
1567	CONSTRUCTION OF 123 BLOCKS IN TELEGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH ,	07/2014	232.00 -	232.00	.00	- -	-	-	0/0
1568	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH ,	08/2007	246.90 -	246.90	.00	- -	-	-	0/0
1569	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP - [N28000108]CPWD,ANDHRA PRADESH ,	01/2018	206.58 -	206.58	185.77	03/2019 -	-	-	7/7
1570	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUIDEM A.P. - [N28000133]CPWD,ANDHRA PRADESH ,	02/2019	186.00 199.00	186.00	38.35	09/2020 -	09/2020	0(O) -	1/7
1571	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR ,	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72(O) -	0/0
1572	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR ,	02/2016	496.18 496.00	498.99	118.00	06/2017 -	03/2021	45(O) -	0/5
1573	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI ,	09/2011	38,585.00 -	38,585.00	34,763.00	03/2016 -	-	-	0/0
1574	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI ,	10/2013	1,219.21 -	2,000.00	436.20	10/2019 -	03/2021	17(O) -	0/7
1575	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI ,	07/2012	884.30 -	884.30	746.48	12/2015 -	-	-	0/0
1576	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI ,	06/2012	4,264.00 4,720.73	4,720.73	4,553.13	11/2019 03/2020	05/2020	6(O) 2	3/7
1577	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG NEW DELHI - [N28000087]CPWD,DELHI ,	06/2015	197.33 -	197.33	67.09	04/2019 -	12/2020	20(O) -	1/2

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1578	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI ,	07/2016	2,694.00 -	2,694.00	.00	- -	-	-	0/0
1579	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS MINTO ROAD NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD,DELHI ,	11/2017	238.56 -	238.56	63.67	05/2020 -	05/2020	0(O) -	1/2
1580	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI ,	10/2016	422.00 -	422.00	15.11	- 03/2021	12/2020	- 0	0/0
1581	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI ,	10/2016	392.00 -	392.00	13.90	- 08/2020	03/2021	- 0	0/0
1582	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI ,	10/2016	248.20 -	248.20	52.95	04/2018 02/2020	08/2020	28(O) 0	0/0
1583	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI ,	10/2017	271.90 -	271.90	65.00	11/2019 08/2020	08/2020	9(O) 0	0/0
1584	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI - [N28000123]CPWD,DELHI ,	07/2017	218.72 218.72	218.72	57.71	- -	-	-	0/2
1585	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I - [N28000128]CPWD,DELHI ,	10/2016	1,180.00 -	1,100.80	9.96	07/2021 -	07/2021	0(O) -	0/0
1586	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]CPWD,DELHI ,	10/2016	1,128.00 -	1,128.00	1.52	03/2022 -	03/2022	0(O) -	0/0
1587	CONSTRUCTION OF GRAMEEN VIKAS BHAWAN (2BASEMENTS+ GROUND+9 FLOORS) FOR MINISTRY OF RURAL DEVELOPMENT - [N28000132]CPWD,DELHI ,	11/2018	361.60 -	361.60	.45	07/2021 -	07/2021	0(O) -	0/2
1588	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS - [N28000135]DMRC,DELHI ,	07/2019	24,948.65 -	24,948.65	78.44	03/2025 -	03/2025	0(O) -	0/0
1589	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136]DMRC,DELHI ,	05/2017	565.00 -	565.00	420.66	12/2020 -	12/2020	0(O) -	0/0
1590	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR GUJARAT - [N12000106]HSCL,GUJARAT ,	01/2013	175.00 -	175.00	1.83	- -	-	-	0/0
1591	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT ,	11/2014	10,773.00 -	10,773.00	6,532.69	12/2018 -	07/2020	19(O) -	0/0
1592	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137]MEGA,GUJARAT ,	03/2019	5,384.17 -	5,384.17	4.35	03/2024 -	03/2024	0(O) -	0/0
1593	SURAT METRO RAIL PROJECT - [N28000138]MEGA,GUJARAT ,	03/2019	12,020.32 -	12,020.32	4.67	03/2024 -	03/2024	0(O) -	0/0
1594	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH ,	11/2012	270.83 -	270.83	199.91	11/2014 -	-	-	2/8
1595	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD,HIMACHAL PRADESH ,	12/2018	260.00 -	260.00	12.50	06/2021 -	06/2021	0(O) -	0/0
1596	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130]CPWD,JAMMU AND KASHMIR ,	03/2019	329.00 -	329.00	.00	- -	-	-	0/0
1597	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]CPWD,JAMMU AND KASHMIR ,	01/2018	676.00 -	676.00	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1598	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND ,	12/2007	253.92 253.92	253.92	193.97	06/2016 -	-	-	0/0
1599	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI KODERMA HAZARIBAG RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND ,	12/2007	200.00 -	200.00	131.15	03/2018 -	-	-	0/0
1600	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND ,	02/2014	787.29 -	787.29	285.30	12/2016 -	-	-	0/0
1601	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND ,	04/2013	170.00 -	170.00	88.91	04/2018 -	-	-	0/0
1602	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND ,	09/2012	171.86 -	171.86	97.70	03/2016 -	09/2020	54(O) -	1/6
1603	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA ,	05/2005	768.88 1,070.97	1,113.34	1,085.64	02/2014 -	-	-	0/0
1604	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA ,	07/2011	324.87 324.87	324.87	262.93	12/2015 -	-	-	0/0
1605	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA ,	02/2014	26,405.14 -	26,405.14	499.85	02/2019 -	03/2020	13(O) -	0/0
1606	RESIDENTIAL QUATERS FOR HAL BANGLORE - [N28000103]CPWD,KARNATAKA ,	12/2016	246.31 -	246.31	85.43	02/2020 -	09/2020	7(O) -	0/10
1607	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA ,	01/2010	165.23 -	165.23	100.81	10/2012 -	03/2020	89(O) -	1/8
1608	KOCHI METRO RAIL PROJECT - [N28000081]KMRL,KERALA ,	07/2012	5,181.79 5,687.79	6,218.14	5,817.11	07/2017 -	03/2020	32(O) -	0/0
1609	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST - [N28000112]CPWD,KERALA ,	09/2017	150.29 -	150.29	21.82	03/2020 11/2020	03/2021	12(O) 0	2/7
1610	BHOPAL METRO RAIL - [N28000124]JPMRCL,MADHYA PRADESH ,	11/2018	6,941.40 -	6,941.40	58.37	02/2023 -	02/2023	0(O) -	0/0
1611	INDORE METRO RAIL - [N28000125]JPMRCL,MADHYA PRADESH ,	11/2018	7,500.80 -	7,500.80	54.74	02/2023 -	02/2023	0(O) -	0/0
1612	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD,MAHARASHTRA ,	06/2010	205.00 -	205.00	166.12	03/2012 -	12/2019	-	20/20
1613	NAGPUR METRO RAIL - [N28000085]NMRL,MAHARASHTRA ,	08/2014	8,680.00 -	8,680.00	6,639.30	03/2018 -	12/2019	-	0/0
1614	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]JMMRCL,MAHARASHTRA ,	07/2013	23,136.00 -	23,136.00	.00	01/2015 -	05/2020	64(O) -	0/0
1615	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY POWAI MUMBAI - [N28000117]CPWD,MAHARASHTRA ,	01/2018	223.37 -	223.37	48.89	07/2020 12/2020	12/2020	5(O) 0	4/14
1616	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]JMMRCL,MAHARASHTRA ,	12/2016	11,420.00 11,420.00	11,420.00	3,614.06	11/2021 03/2022	03/2022	4(O) 0	0/0
1617	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR , Central Sector Projects	02/2014	216.69 -	216.69	52.00	03/2015 -	10/2020	67(O) -	0/10
1618	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE SHILONG IN MEGALAYA UNDER NLCP - [N12000103]HSCL,MEGHALAYA ,	04/2014	151.33 -	151.33	7.15	09/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1619	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134]NCRTC,MULTI STATE ,	03/2019	30,274.00 -	30,274.00	690.64	06/2025 -	06/2025	0(O) -	0/0
1620	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD,ODISHA ,	01/2019	790.79 -	790.79	41.06	03/2022 06/2022	06/2022	3(O) 0	0/5
1621	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT - [N28000139]CPWD,PONDICHERRY ,	03/2018	195.00 -	195.00	.00	09/2020 -	01/2021	4(O) -	0/33
1622	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR PUNJAB - [N28000088]CPWD,PUNJAB ,	02/2014	388.00 500.18	490.00	442.51	05/2017 -	03/2020	34(O) -	8/12
1623	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR PUNJAB - [N28000102]CPWD,PUNJAB ,	08/2016	294.00 350.69	350.69	219.60	04/2019 -	05/2020	13(O) -	7/8
1624	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR PUNJAB - [N28000120]CPWD,PUNJAB ,	01/2018	430.00 387.83	387.83	124.24	05/2020 -	02/2021	9(O) -	1/5
1625	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN ,	05/2015	189.00 -	189.00	.00	03/2017 -	-	-	0/0
1626	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN ,	12/2016	549.31 559.47	559.47	373.45	07/2019 03/2020	08/2020	13(O) 4	2/6
1627	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU ,	02/2009	14,600.00 -	19,058.00	16,352.87	12/2015 -	-	-	12/24
1628	C/O OF 152 NOS TYPE-II 304 NOS TYPE-III 76 NOS TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD,TAMIL NADU ,	12/2015	209.00 -	209.00	150.71	10/2019 -	07/2020	9(O) -	1/6
1629	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU ,	06/2016	3,770.00 -	3,770.00	2,258.91	03/2018 06/2020	06/2020	27(O) 0	5/21
1630	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU ,	11/2017	348.77 -	348.77	31.98	- -	11/2021	- -	0/8
1631	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA ,	10/2016	209.84 -	209.84	70.43	03/2020 -	05/2021	14(O) -	1/5
1632	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA ,	03/2007	149.73 173.00	175.94	176.65	12/2015 -	-	-	0/0
1633	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA ,	12/2007	202.61 227.00	227.00	199.95	12/2016 -	-	-	0/0
1634	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA ,	10/2011	175.49 206.71	206.71	141.28	12/2016 -	-	-	0/0
1635	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH ,	01/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 -	-	-	0/0
1636	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH ,	11/2017	171.72 -	171.72	45.00	03/2020 11/2020	03/2020	0(O) 0	0/0
1637	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND ,	12/2008	114.26 266.00	266.00	.00	12/2013 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1638	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL, WEST BENGAL , Central Sector Projects	08/2012	185.37 -	185.37	178.30	03/2016 -	-	-	0/0
1639	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD, WEST BENGAL ,	02/2014	156.57 -	156.57	159.35	08/2016 -	01/2020	41(O) -	16/16
1640	NSG AT KOLKATA - [N28000104]CPWD, WEST BENGAL , Central Sector Projects	10/2014	162.88 179.10	162.88	148.52	04/2018 06/2020	06/2020	26(O) 0	5/6
	Total		2,63,824.96 -	2,71,185.14	92,748.02				101/279
	<u>WATER RESOURCES</u>								
1641	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA, ANDHRA PRADESH , National Project	02/2009	10,151.04 55,548.87	55,548.87	32,535.80	03/2020 11/2019	12/2021	21(O) 6	0/19
1642	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026]BUIDCO, BIHAR ,	03/2018	230.06 -	230.06	.00	07/2021 -	07/2021	0(O) -	0/0
1643	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO, BIHAR ,	10/2017	254.13 -	254.13	.05	09/2020 -	09/2020	0(O) -	0/0
1644	I AND D AND STP AT CHAPRA - [N30000028]BUIDCO, BIHAR ,	11/2018	236.15 -	236.15	.06	12/2020 -	12/2020	0(O) -	0/0
1645	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]BUIDCO, BIHAR ,	03/2018	305.19 -	305.19	.00	08/2021 -	08/2021	0(O) -	0/0
1646	SEWER NETWORKS SPS AND STP MUNGER - [N30000036]BUIDCO, BIHAR ,	03/2018	294.02 -	294.02	.00	10/2021 -	10/2021	0(O) -	0/0
1647	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]BUIDCO, BIHAR ,	12/2014	225.77 -	225.77	183.57	03/2020 -	03/2020	0(O) -	0/0
1648	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR - [N30000038]BUIDCO, BIHAR ,	04/2015	184.93 -	184.93	163.36	04/2020 -	04/2020	0(O) -	0/0
1649	SAIDPUR SEWER NETWORK PATNA - [N30000039]BUIDCO, BIHAR ,	04/2015	268.63 -	268.63	192.80	01/2021 -	01/2021	0(O) -	0/0
1650	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]BUIDCO, BIHAR ,	05/2017	356.37 -	356.37	66.44	04/2021 -	04/2021	0(O) -	0/0
1651	SEWERAGE SCHEME AT PAHARI ZONE IVA S PATNA - [N30000041]BUIDCO, BIHAR ,	05/2017	184.86 -	184.86	103.13	05/2021 -	05/2021	0(O) -	0/0
1652	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]BUIDCO, BIHAR ,	05/2017	191.62 -	191.62	37.70	11/2020 -	11/2020	0(O) -	0/0
1653	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]BUIDCO, BIHAR ,	03/2017	277.42 -	277.42	85.87	05/2021 -	05/2021	0(O) -	0/0
1654	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]BUIDCO, BIHAR ,	08/2017	578.89 -	578.89	.29	06/2022 -	06/2022	0(O) -	0/0
1655	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE PATNA - [N30000051]BUIDCO, BIHAR ,	08/2017	824.00 -	824.00	.41	06/2022 -	06/2022	0(O) -	0/0
1656	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014]DJB, DELHI ,	03/2017	665.78 -	665.78	94.40	12/2022 -	12/2022	0(O) -	0/0
1657	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015]DJB, DELHI ,	05/2016	211.79 -	211.79	39.14	12/2021 -	12/2021	0(O) -	0/0
1658	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]DJB, DELHI ,	05/2016	239.11 -	239.11	42.77	02/2022 -	02/2022	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1659	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND MAT CORONATION PILLAR DELHI - [N30000017]DJB,DELHI ,	12/2018	515.07 -	515.07	246.01	01/2021 -	01/2021	0(O) -	0/0
1660	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018]DJB,DELHI ,	05/2017	344.81 -	344.81	.00	05/2020 -	05/2020	0(O) -	0/0
1661	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPB,MAHARASHTRA ,	03/2017	233.57 -	233.57	32.20	12/2019 -	-	-	0/0
1662	INTERCEPTION DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006]UPJalNigam,UTTAR PRADESH ,	05/2017	767.59 -	767.59	.01	09/2021 -	09/2021	0(O) -	0/0
1663	INTEGRATED PROJECT FOR DEVELOPMENT OF STPS IN ALLAHABAD ALONG WITH EXISTING ASSETS - [N30000007]UPJalNigam,UTTAR PRADESH ,	03/2018	904.00 -	904.00	.00	09/2021 -	09/2021	0(O) -	0/0
1664	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]UPJalNigam,UTTAR PRADESH ,	10/2017	213.62 -	213.62	.00	03/2022 -	03/2022	0(O) -	0/0
1665	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR - [N30000009]UPJalNigam,UTTAR PRADESH ,	10/2016	370.40 430.49	370.40	268.59	08/2020 -	08/2020	0(O) -	0/0
1666	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010]UPJalNigam,UTTAR PRADESH ,	03/2018	967.23 -	967.23	.00	09/2021 -	09/2021	0(O) -	0/0
1667	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA - [N30000011]UPJalNigam,UTTAR PRADESH ,	02/2017	161.31 -	161.31	37.60	11/2019 02/2020	02/2020	3(O) 0	0/0
1668	REHABILITATION RENOVATION OF AGRA SEWERAGE SCHEME INTERCEPTION AND DIVERSION WORKS IN AGRA UTTAR PR - [N30000012]UPJalNigam,UTTAR PRADESH ,	12/2018	857.26 -	857.26	.00	08/2021 -	08/2021	0(O) -	0/0
1669	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY UTTAR PRADESH - [N30000013]UPJalNigam,UTTAR PRADESH ,	03/2019	271.39 -	271.39	.00	08/2021 -	08/2021	0(O) -	0/0
1670	MATHURA SEWERAGE SCHEME - [N30000019]UPJalNigam,UTTAR PRADESH ,	12/2017	460.45 -	460.45	56.83	12/2020 -	12/2020	0(O) -	0/0
1671	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020]UPJalNigam,UTTAR PRADESH ,	02/2011	279.91 -	279.91	199.59	12/2019 03/2020	03/2020	3(O) 0	0/0
1672	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]UPJalNigam,UTTAR PRADESH ,	01/2019	231.79 -	231.79	.00	12/2021 -	12/2021	0(O) -	0/0
1673	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022]UPJalNigam,UTTAR PRADESH ,	01/2019	206.05 -	206.05	1.57	10/2021 -	10/2021	0(O) -	0/0
1674	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WORKS AT AGRA - [N30000023]UPJalNigam,UTTAR PRADESH ,	02/2019	317.19 -	317.19	.00	08/2021 -	08/2021	0(O) -	0/0
1675	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]UPJalNigam,UTTAR PRADESH ,	02/2019	681.78 -	681.78	.00	06/2022 -	06/2022	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(January 2020)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1676	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]UPJalNigam,UTTAR PRADESH ,	03/2019	298.12 -	298.12	.00	07/2021 -	07/2021	0(O) -	0/0
1677	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI - [N30000003]UKJalNigam,UTTARAKHAND ,	03/2017	273.37 -	273.37	53.19	08/2019 02/2020	02/2020	6(O) 0	0/0
1678	INTERCEPTION AND DIVERSION (I&D)WITH STP AT RISHIKESH - [N30000004]UKJalNigam,UTTARAKHAND ,	03/2017	158.00 -	158.00	.00	11/2019 -	-	-	0/0
1679	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]KMDA, WEST BENGAL ,	01/2019	384.96 -	384.96	.00	04/2022 -	04/2022	0(O) -	0/0
1680	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPUR - [N30000030]KMDA, WEST BENGAL ,	03/2019	287.53 -	287.53	.00	04/2022 -	04/2022	0(O) -	0/0
1681	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]KMDA, WEST BENGAL ,	12/2018	234.31 -	234.31	.00	04/2022 -	04/2022	0(O) -	0/0
1682	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]KMDA, WEST BENGAL ,	05/2018	198.43 -	198.43	.00	02/2022 -	02/2022	0(O) -	0/0
1683	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033]KMDA, WEST BENGAL ,	03/2018	165.16 -	165.16	.00	06/2022 -	06/2022	0(O) -	0/0
1684	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA - [N30000034]KMDA, WEST BENGAL ,	08/2017	307.12 -	307.12	.00	09/2022 -	09/2022	0(O) -	0/0
1685	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH - [N30000042]KMDA, WEST BENGAL ,	05/2018	160.00 -	160.00	.00	02/2022 -	02/2022	0(O) -	0/0
1686	INTERCEPTION DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]KMDA, WEST BENGAL ,	08/2017	185.22 -	185.22	.00	12/2021 -	12/2021	0(O) -	0/0
1687	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046]KMDA, WEST BENGAL ,	02/2014	274.76 -	274.76	171.80	12/2019 02/2020	02/2020	2(O) 0	0/0
1688	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]KMDA, WEST BENGAL ,	12/2014	272.32 -	272.32	191.36	04/2020 -	04/2020	0(O) -	0/0
1689	INTERCEPTION DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048]KMDA, WEST BENGAL ,	01/2018	172.10 -	172.10	.00	12/2021 -	12/2021	0(O) -	0/0
1690	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]KMDA, WEST BENGAL ,	10/2017	164.93 -	164.93	.00	12/2021 -	12/2021	0(O) -	0/0
	Total		26,999.51 -	72,397.34	34,804.54				0/19
	<u>COMMERCE AND INDUSTRY</u>								
1691	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]IICC, DELHI ,	11/2017	4,773.00 -	5,178.00	1,309.65	12/2019 -	09/2020	9(O) -	0/0
1692	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]DMIC, MULTI STATE ,	09/2011	12,579.09 -	12,579.09	778.93	09/2019 -	09/2020	12(O) -	0/0
	Total		17,352.09 -	17,757.09	2,088.58				0/0
	Grand Total		20,75,212..70	24,78,016.45	10,97,604.64				2953/5636


Summary of projects in the Flash Report for the month of January, 2020

Project Implementation - Current Status:

Number of Projects in Previous Month	1701
Number of Projects completed/dropped/frozen in Current Month	13
Number of Projects elevated to the status of Major project during the current month	1
Number of Projects Added in Current Month	5
Number of Projects in Current Month	1692

Brief Analysis


Project Status with respect to Original Schedule: Out of 1692 projects, 14 projects are ahead of schedule, 302 projects are on schedule 552 projects are delayed. 666 projects do not have fixed dates of commissioning. 158 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

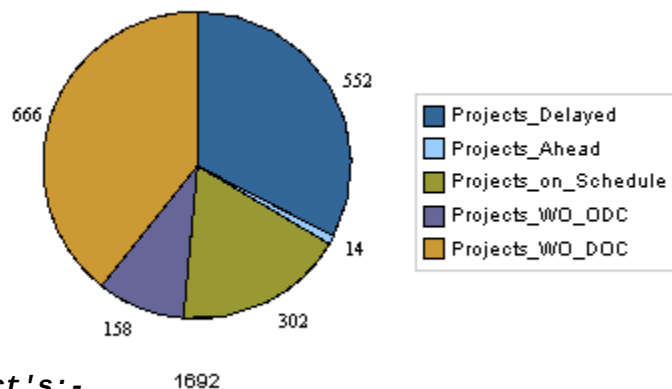

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1692 projects when sanctioned, was of the order of Rs. 2075212.7 crore but this was subsequently revised to Rs. 2478016.45 crore implying a cost overrun of 19.4%. The expenditure incurred on these projects till January, 2020 is Rs. 1097604.64 crore, which is 44.3% of the anticipated cost of the projects.

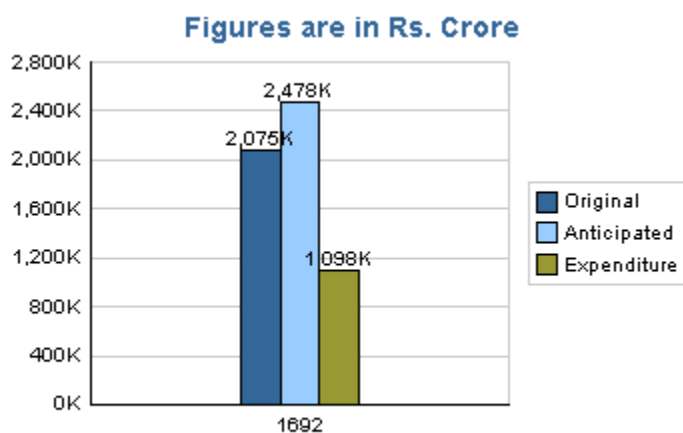

Sector wise current status of projects on the Flash Report


COMMERCE AND INDUSTRY

Current Status:

Number of Projects	2
Number of Projects Delayed	2

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 2 projects are delayed.




Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 17352.09 crore but this was subsequently anticipated to Rs. 17757.09 crore implying a cost overrun of 2.3%. The expenditure incurred on these projects till January, 2020 is Rs. 2088.58 crore, which is 11.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

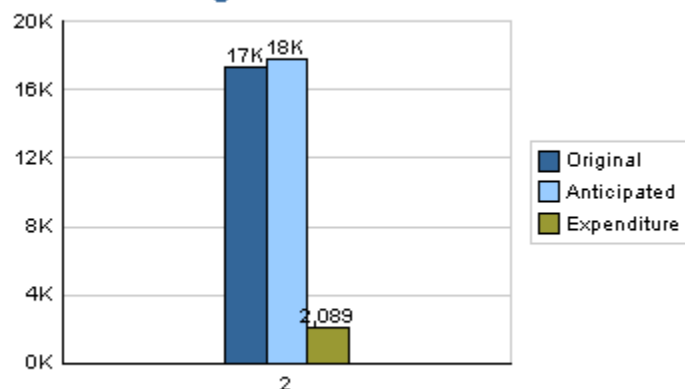

Sector wise current status of projects on the Flash Report

WATER RESOURCES


Current Status:

Number of Projects	50
Number of Projects On Schedule	43
Number of Projects Delayed	5

Number of Projects Without Date Of Commissioning	2
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 50 projects, 43 projects are on schedule 5 projects are delayed. 2 projects do not have fixed dates of commissioning.

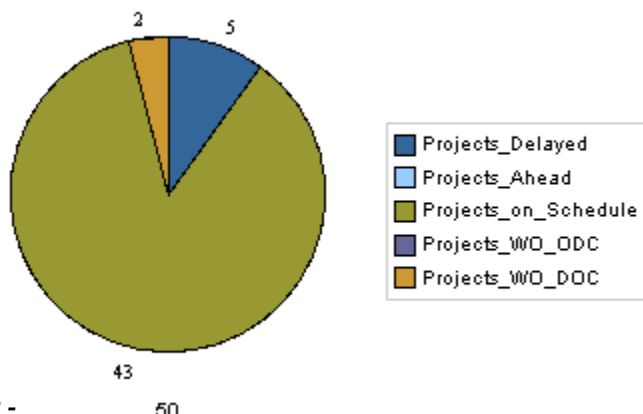


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 50 projects when sanctioned, was of the order of Rs. 26999.51 crore but this was subsequently anticipated to Rs. 72397.34 crore implying a cost overrun of 168.1%. The expenditure incurred on these projects till January, 2020 is Rs. 34804.54 crore, which is 48.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

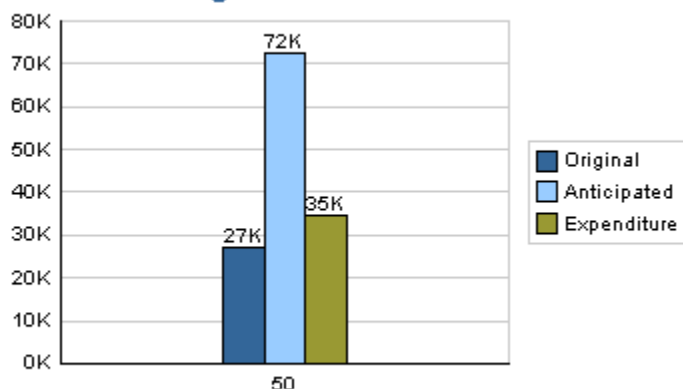

Sector wise current status of projects on the Flash Report


URBAN DEVELOPMENT

Current Status:

Number of Projects	74
Number of Projects On Schedule	14
Number of Projects Delayed	29
Number of Projects Without Original Date of Commissioning	3
Number of Projects Without Date Of Commissioning	28

Brief Analysis

Project Status with respect to Original Schedule: Out of 74 projects, 14 projects are on schedule 29 projects are delayed. 28 projects do not have fixed dates of commissioning. 3 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

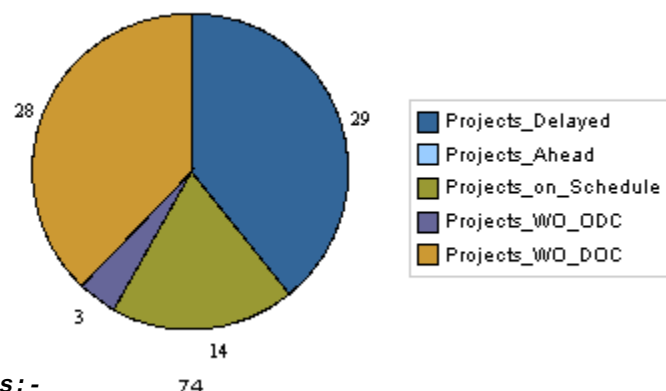


Total No Of Project's:-

74

Investment Scenario

Total original cost of implementation of 74 projects when sanctioned, was of the order of Rs. 263824.96 crore but this was subsequently anticipated to Rs. 271185.14 crore implying a cost overrun of 2.8%. The expenditure incurred on these projects till January, 2020 is Rs. 92748.02 crore, which is 34.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

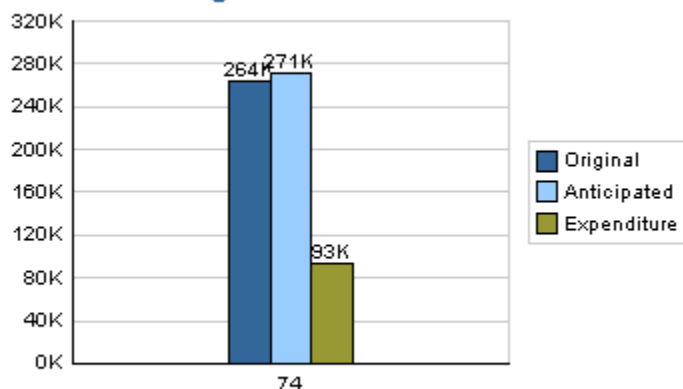

Sector wise current status of projects on the Flash Report

TELECOMMUNICATIONS

Current Status:


Number of Projects 4

Number of Projects Delayed 2

Number of Projects Without Date Of Commissioning 2

Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 2 projects are delayed. 2 projects do not have fixed dates of commissioning.

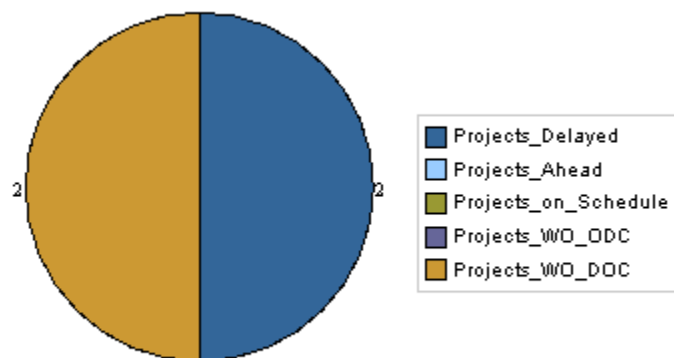


Total No Of Project's:-

4

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 16095.23 crore but this was subsequently anticipated to Rs. 27333.53 crore implying a cost overrun of 69.8%. The expenditure incurred on these projects till January, 2020 is Rs. 12886.86 crore, which is 47.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

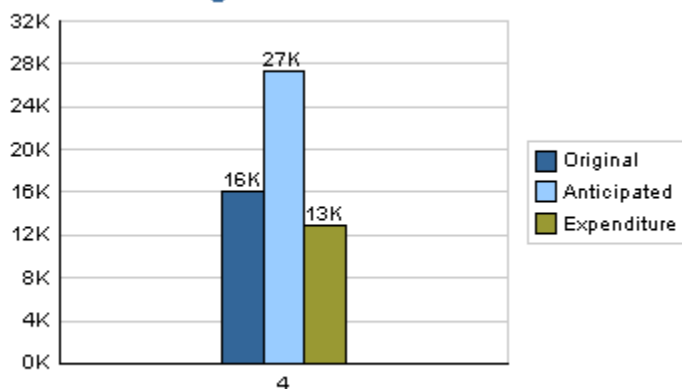

Sector wise current status of projects on the Flash Report


SHIPPING AND PORTS

Current Status:

Number of Projects	1
Number of Projects On Schedule	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 1 project, 1 project is on schedule

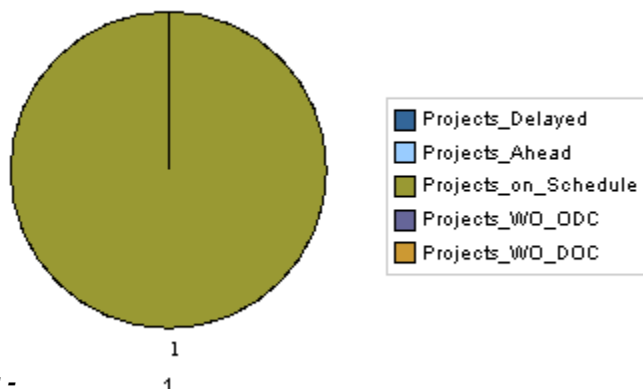


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 4200 crore but this was subsequently anticipated to Rs. 5369.18 crore implying a cost overrun of 27.8%. The expenditure incurred on these projects till January, 2020 is Rs. 1540.69 crore, which is 28.7% of the anticipated cost of the projects.

Figures are in Rs. Crore

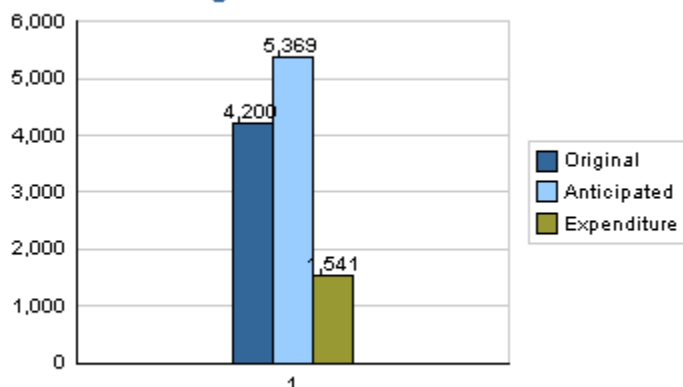

Sector wise current status of projects on the Flash Report


ROAD TRANSPORT AND HIGHWAYS

Current Status:

Number of Projects	867
Number of Projects On Schedule	59
Number of Projects Delayed	186
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	96
Number of Projects Without Date Of Commissioning	525

Brief Analysis

Project Status with respect to Original Schedule: Out of 867 projects, 1 project is ahead of schedule, 59 projects are on schedule 186 projects are delayed. 525 projects do not have fixed dates of commissioning. 96 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

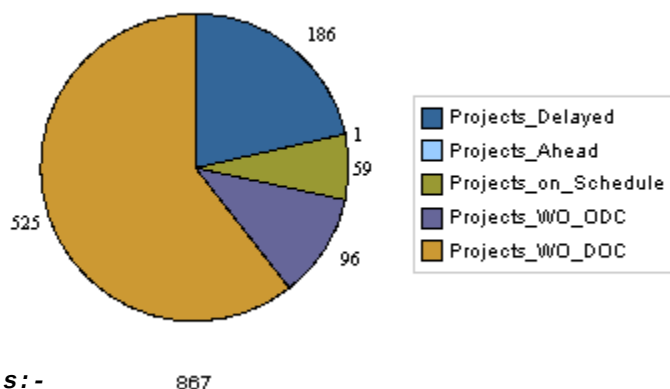


Total No Of Project's:-

867

Investment Scenario

Total original cost of implementation of 867 projects when sanctioned, was of the order of Rs. 513537.42 crore but this was subsequently anticipated to Rs. 528085.9 crore implying a cost overrun of 2.8%. The expenditure incurred on these projects till January, 2020 is Rs. 300798.25 crore, which is 57% of the anticipated cost of the projects.

Figures are in Rs. Crore

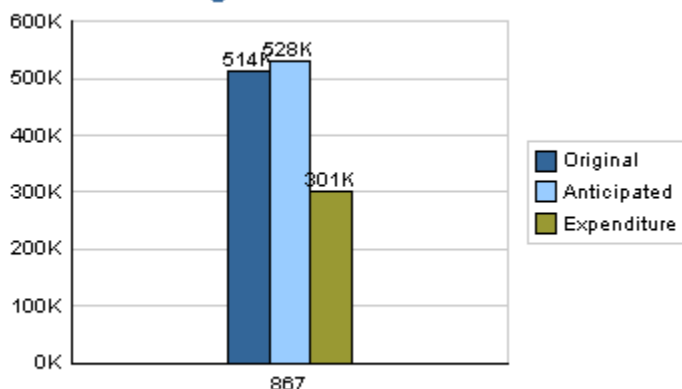

Sector wise current status of projects on the Flash Report


RAILWAYS

Current Status:

Number of Projects	312
Number of Projects On Schedule	35
Number of Projects Delayed	148
Number of Projects Ahead	6
Number of Projects Without Original Date of Commissioning	48
Number of Projects Without Date Of Commissioning	75

Brief Analysis

Project Status with respect to Original Schedule: Out of 312 projects, 6 projects are ahead of schedule, 35 projects are on schedule 148 projects are delayed. 75 projects do not have fixed dates of commissioning. 48 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

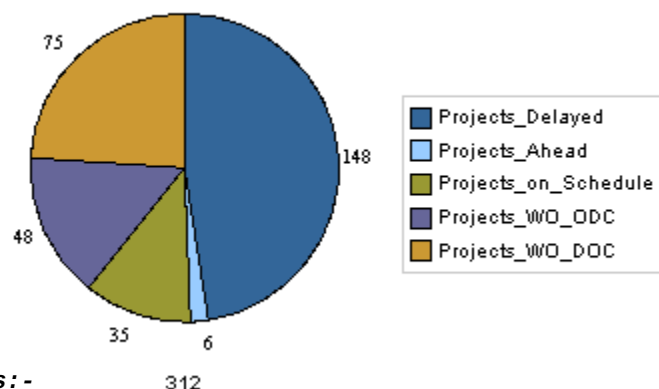


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 312 projects when sanctioned, was of the order of Rs. 459394.75 crore but this was subsequently anticipated to Rs. 671692.95 crore implying a cost overrun of 46.2%. The expenditure incurred on these projects till January, 2020 is Rs. 206153.91 crore, which is 30.7% of the anticipated cost of the projects.

Figures are in Rs. Crore

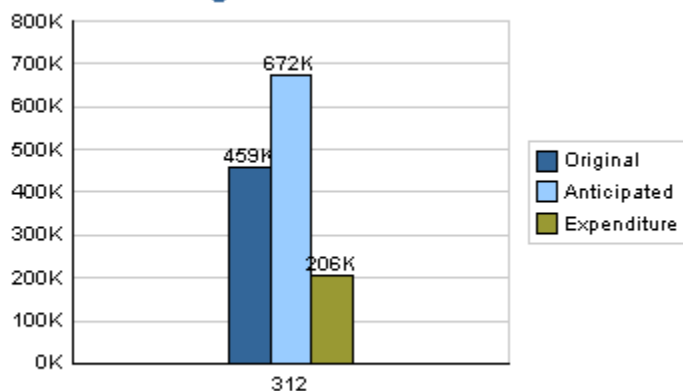

Sector wise current status of projects on the Flash Report

HEALTH AND FAMILY WELFARE


Current Status:

Number of Projects	23
Number of Projects On Schedule	3
Number of Projects Delayed	11

Number of Projects Without Original Date of Commissioning	6
Number of Projects Without Date Of Commissioning	3

Brief Analysis

Project Status with respect to Original Schedule: Out of 23 projects, 3 projects are on schedule 11 projects are delayed. 3 projects do not have fixed dates of commissioning. 6 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

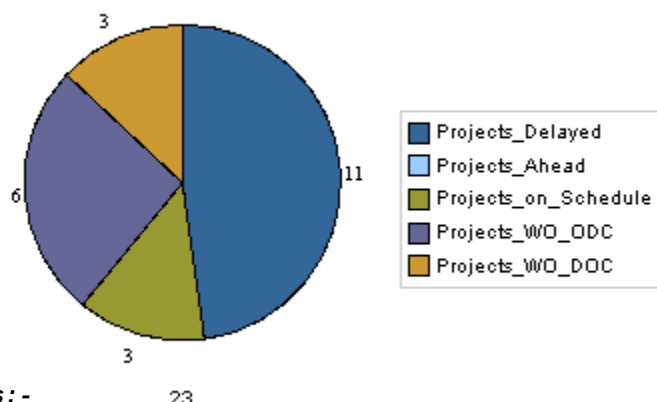


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 23 projects when sanctioned, was of the order of Rs. 12454.56 crore but this was subsequently anticipated to Rs. 12796.11 crore implying a cost overrun of 2.7%. The expenditure incurred on these projects till January, 2020 is Rs. 5325.26 crore, which is 41.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

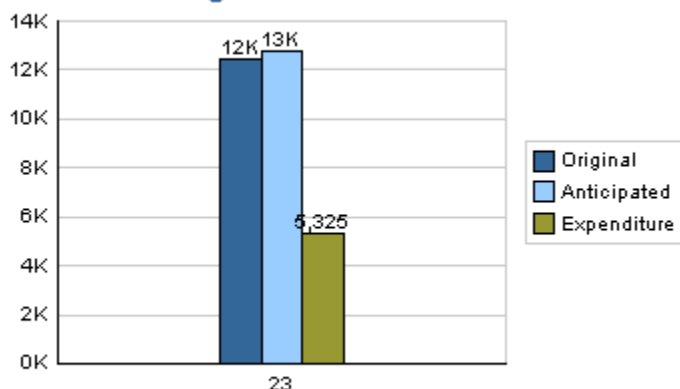

Sector wise current status of projects on the Flash Report


HEAVY INDUSTRY

Current Status:

Number of Projects	1
Number of Projects Delayed	1

Brief Analysis


Project Status with respect to Original Schedule: Out of 1 project, 1 project is delayed.

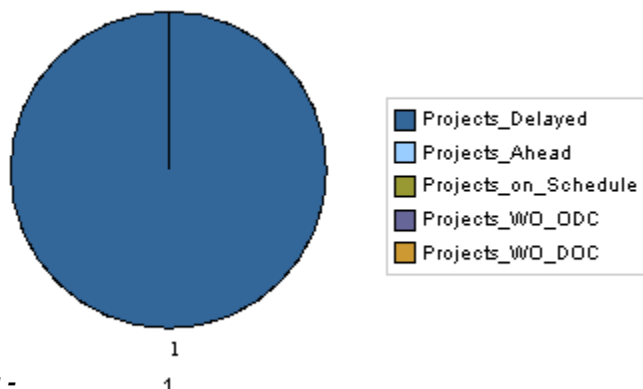

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 1554 crore but this was subsequently anticipated to Rs. 1554 crore. The expenditure incurred on these projects till January, 2020 is Rs. 716.25 crore, which is 46.1% of the anticipated cost of the projects.

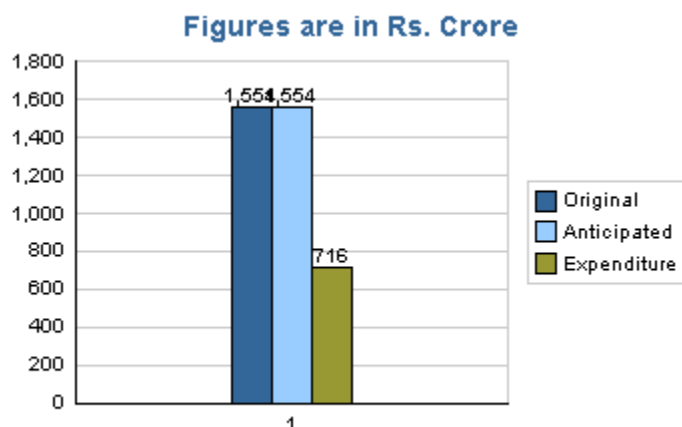

Sector wise current status of projects on the Flash Report

POWER


Current Status:

Number of Projects	64
Number of Projects On Schedule	10
Number of Projects Delayed	48

Number of Projects Without Date Of Commissioning	6
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 64 projects, 10 projects are on schedule 48 projects are delayed. 6 projects do not have fixed dates of commissioning.

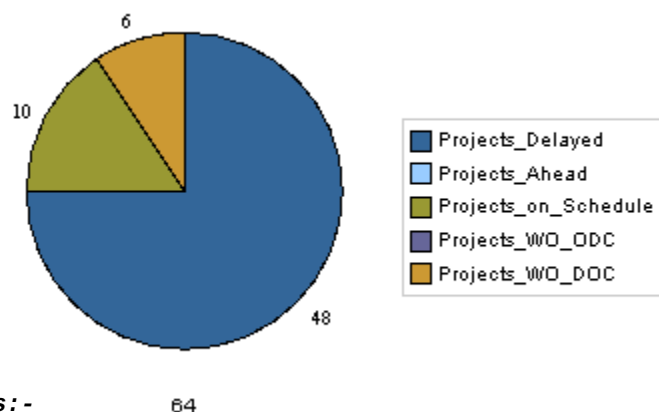


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 64 projects when sanctioned, was of the order of Rs. 273781.33 crore but this was subsequently anticipated to Rs. 344106.51 crore implying a cost overrun of 25.7%. The expenditure incurred on these projects till January, 2020 is Rs. 222894.97 crore, which is 64.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

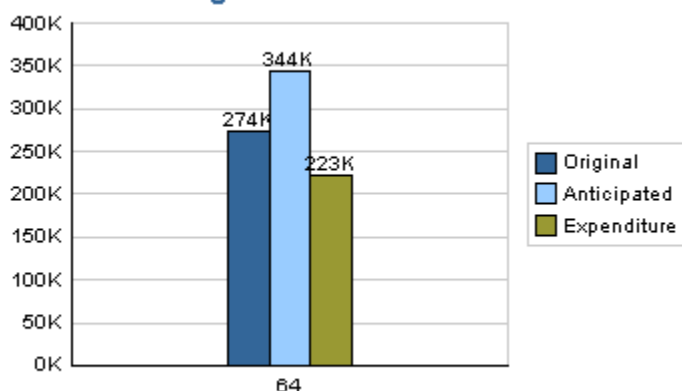

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	148
Number of Projects On Schedule	69
Number of Projects Delayed	60
Number of Projects Ahead	7
Number of Projects Without Original Date of Commissioning	2
Number of Projects Without Date Of Commissioning	10

Brief Analysis

Project Status with respect to Original Schedule: Out of 148 projects, 7 projects are ahead of schedule, 69 projects are on schedule 60 projects are delayed. 10 projects do not have fixed dates of commissioning. 2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

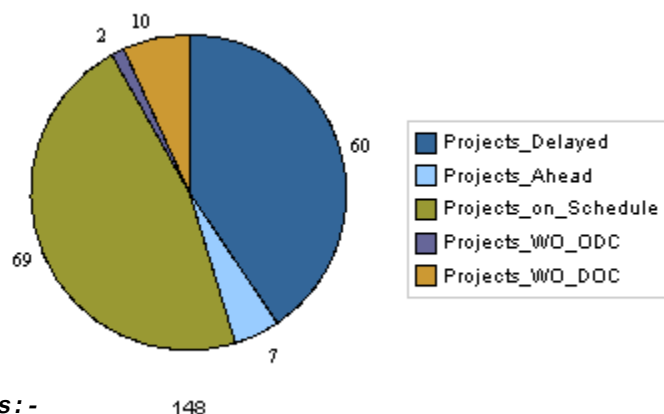


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 148 projects when sanctioned, was of the order of Rs. 269889.88 crore but this was subsequently anticipated to Rs. 284938.4 crore implying a cost overrun of 5.6%. The expenditure incurred on these projects till January, 2020 is Rs. 101562.39 crore, which is 35.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

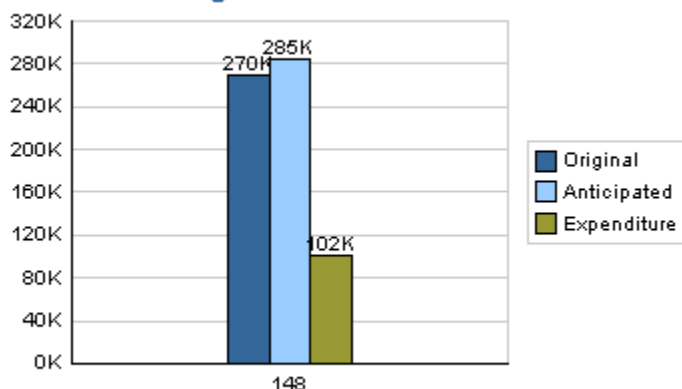

Sector wise current status of projects on the Flash Report


STEEL

Current Status:

Number of Projects	9
Number of Projects On Schedule	1
Number of Projects Delayed	8

Brief Analysis

Project Status with respect to Original Schedule: Out of 9 projects, 1 project is on schedule 8 projects are delayed.

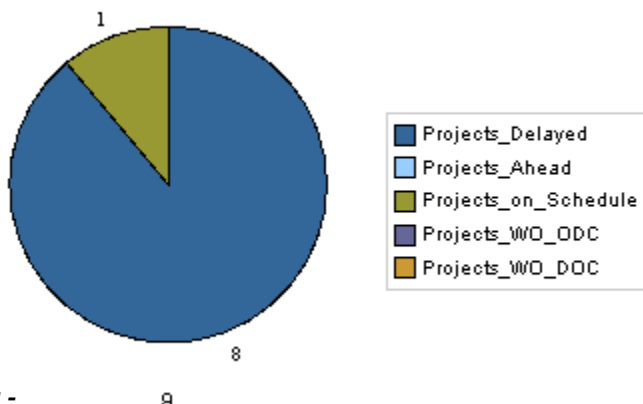


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 9 projects when sanctioned, was of the order of Rs. 26228.23 crore but this was subsequently anticipated to Rs. 33485.23 crore implying a cost overrun of 27.7%. The expenditure incurred on these projects till January, 2020 is Rs. 24413.37 crore, which is 72.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

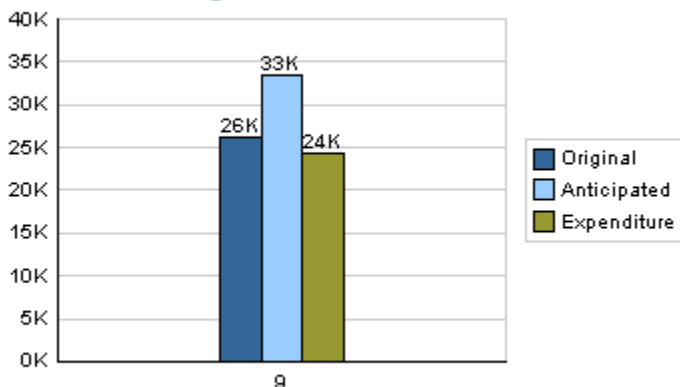

Sector wise current status of projects on the Flash Report


MINES

Current Status:

Number of Projects	5
Number of Projects On Schedule	3
Number of Projects Delayed	2

Brief Analysis

Project Status with respect to Original Schedule: Out of 5 projects, 3 projects are on schedule 2 projects are delayed.

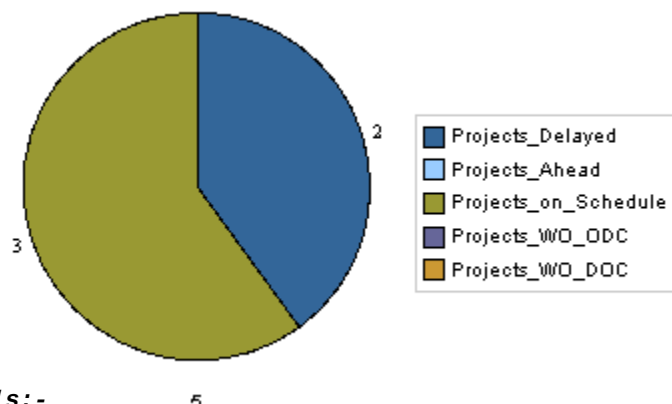


Total No Of Project's:-

5

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 7078.62 crore but this was subsequently anticipated to Rs. 7075.17 crore. The expenditure incurred on these projects till January, 2020 is Rs. 673.31 crore, which is 9.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

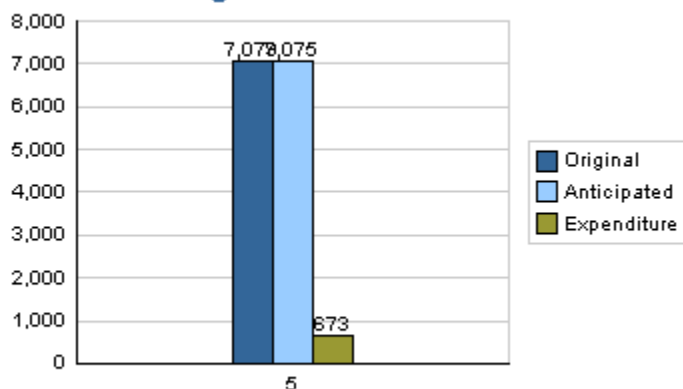

Sector wise current status of projects on the Flash Report

FERTILISERS


Current Status:

Number of Projects	4
Number of Projects On Schedule	1
Number of Projects Delayed	2

Number of Projects Without Date Of Commissioning	1
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 1 project is on schedule 2 projects are delayed. 1 project does not have fixed dates of commissioning.

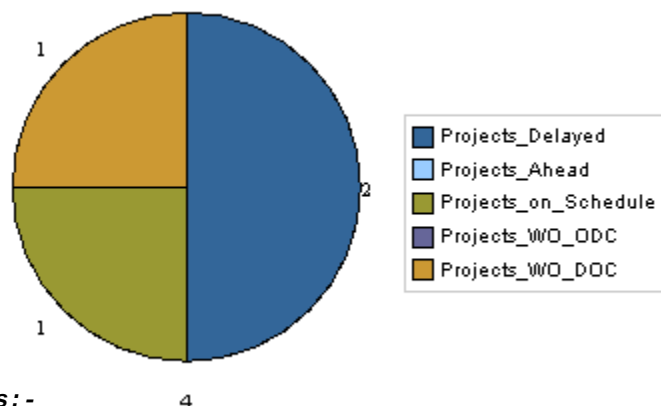

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 1101.28 crore but this was subsequently anticipated to Rs. 1101.28 crore. The expenditure incurred on these projects till January, 2020 is Rs. 701.67 crore, which is 63.7% of the anticipated cost of the projects.

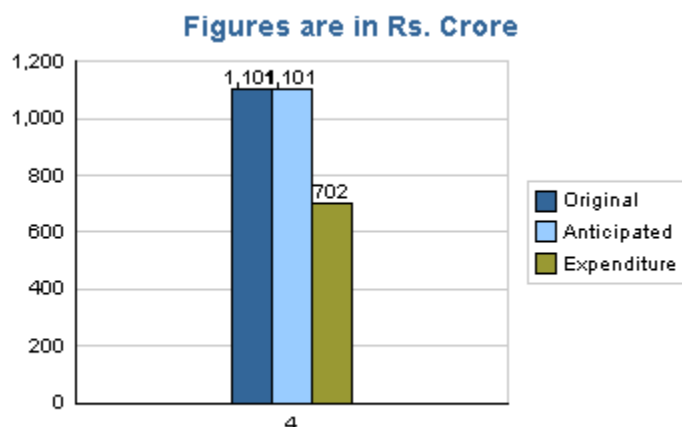

Sector wise current status of projects on the Flash Report

COAL


Current Status:

Number of Projects	107
Number of Projects On Schedule	54
Number of Projects Delayed	39

Number of Projects Without Original Date of Commissioning	3
Number of Projects Without Date Of Commissioning	11

Brief Analysis

Project Status with respect to Original Schedule: Out of 107 projects, 54 projects are on schedule 39 projects are delayed. 11 projects do not have fixed dates of commissioning. 3 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

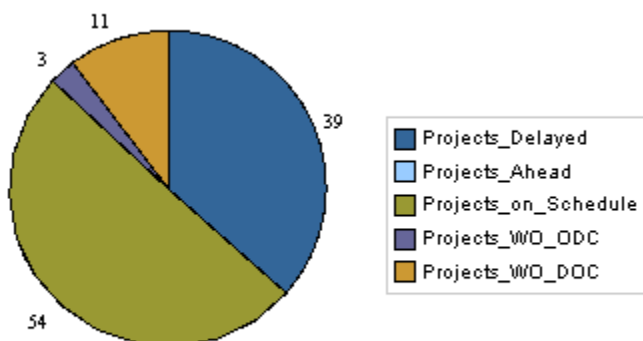


Total No Of Project's:-

107

Investment Scenario

Total original cost of implementation of 107 projects when sanctioned, was of the order of Rs. 104637.11 crore but this was subsequently anticipated to Rs. 108558.02 crore implying a cost overrun of 3.7%. The expenditure incurred on these projects till January, 2020 is Rs. 38613.72 crore, which is 35.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

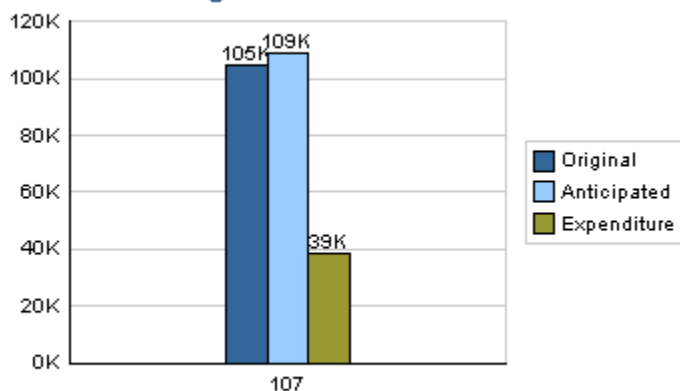

Sector wise current status of projects on the Flash Report

CIVIL AVIATION


Current Status:

Number of Projects	13
Number of Projects On Schedule	8
Number of Projects Delayed	4

Number of Projects Without Date Of Commissioning	1
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 13 projects, 8 projects are on schedule 4 projects are delayed. 1 project does not have fixed dates of commissioning.

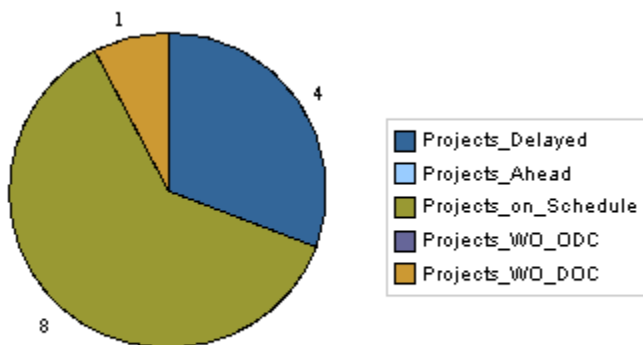


Total No Of Project's:-

13

Investment Scenario

Total original cost of implementation of 13 projects when sanctioned, was of the order of Rs. 8607.51 crore but this was subsequently anticipated to Rs. 8734.44 crore implying a cost overrun of 1.5%. The expenditure incurred on these projects till January, 2020 is Rs. 1357.47 crore, which is 15.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

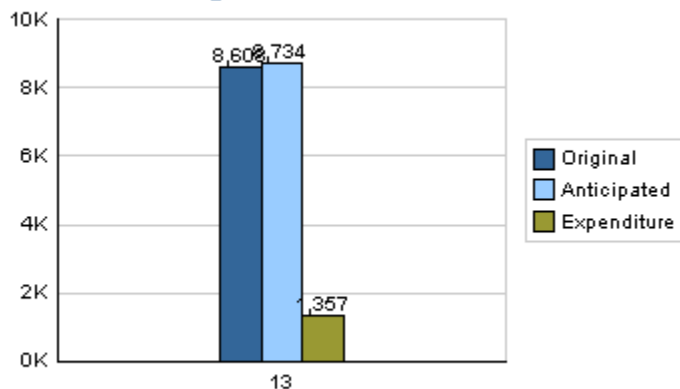

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	4

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed.



Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 67120 crore but this was subsequently anticipated to Rs. 80348 crore implying a cost overrun of 19.7%. The expenditure incurred on these projects till January, 2020 is Rs. 50215.38 crore, which is 62.5% of the anticipated cost of the projects.

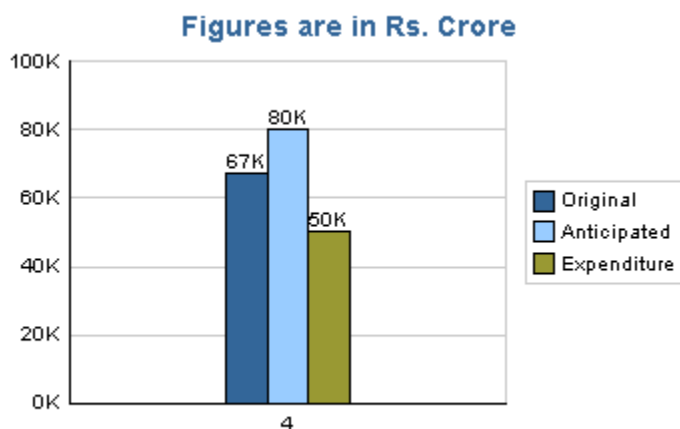

Sector wise current status of projects on the Flash Report


COMMERCE AND INDUSTRY

Current Status:

Number of Projects	2
Number of Projects Delayed	2

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 2 projects are delayed.




Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 17352.09 crore but this was subsequently anticipated to Rs. 17757.09 crore implying a cost overrun of 2.3%. The expenditure incurred on these projects till January, 2020 is Rs. 2088.58 crore, which is 11.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

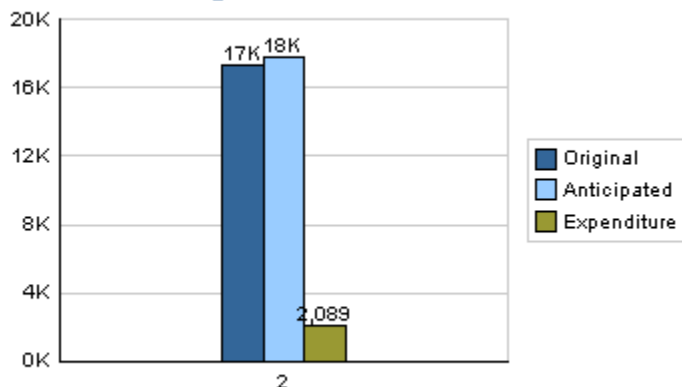

Sector wise current status of projects on the Flash Report

WATER RESOURCES


Current Status:

Number of Projects	50
Number of Projects On Schedule	43
Number of Projects Delayed	5

Number of Projects Without Date Of Commissioning	2
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 50 projects, 43 projects are on schedule 5 projects are delayed. 2 projects do not have fixed dates of commissioning.

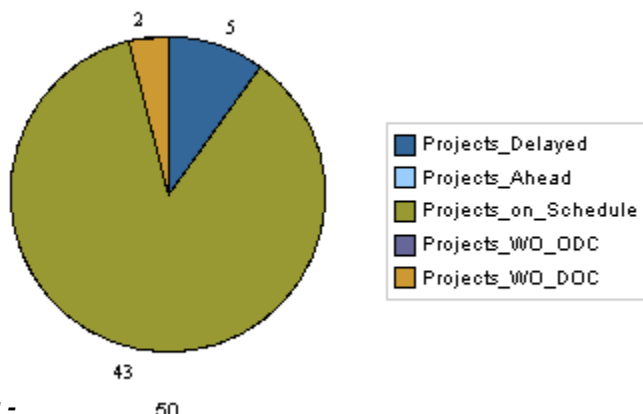


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 50 projects when sanctioned, was of the order of Rs. 26999.51 crore but this was subsequently anticipated to Rs. 72397.34 crore implying a cost overrun of 168.1%. The expenditure incurred on these projects till January, 2020 is Rs. 34804.54 crore, which is 48.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

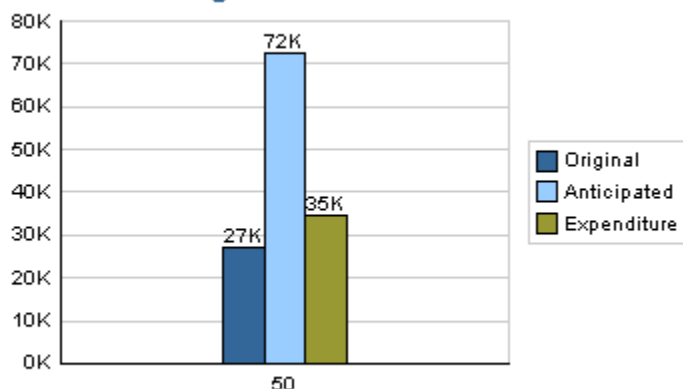

Sector wise current status of projects on the Flash Report

URBAN DEVELOPMENT


Current Status:

Number of Projects	74
Number of Projects On Schedule	14
Number of Projects Delayed	29

Number of Projects Without Original Date of Commissioning	3
Number of Projects Without Date Of Commissioning	28

Brief Analysis

Project Status with respect to Original Schedule: Out of 74 projects, 14 projects are on schedule 29 projects are delayed. 28 projects do not have fixed dates of commissioning. 3 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

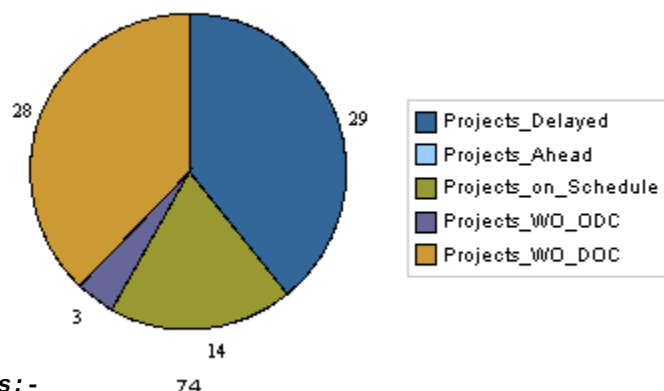


Total No Of Project's:-

74

Investment Scenario

Total original cost of implementation of 74 projects when sanctioned, was of the order of Rs. 263824.96 crore but this was subsequently anticipated to Rs. 271185.14 crore implying a cost overrun of 2.8%. The expenditure incurred on these projects till January, 2020 is Rs. 92748.02 crore, which is 34.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

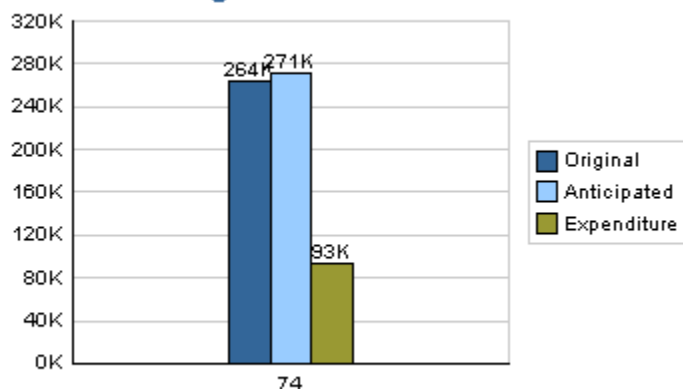

Sector wise current status of projects on the Flash Report

TELECOMMUNICATIONS

Current Status:


Number of Projects 4

Number of Projects Delayed 2

Number of Projects Without Date Of Commissioning 2

Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 2 projects are delayed. 2 projects do not have fixed dates of commissioning.

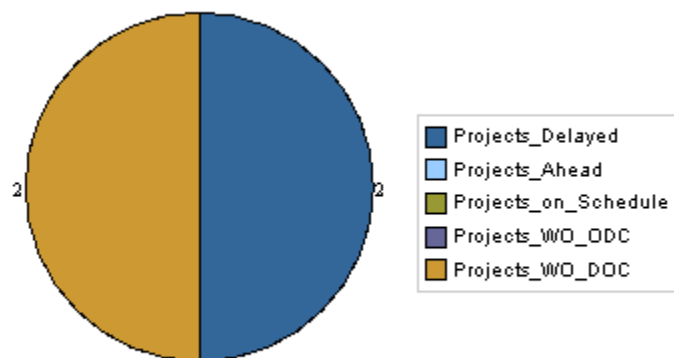


Total No Of Project's:-

4

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 16095.23 crore but this was subsequently anticipated to Rs. 27333.53 crore implying a cost overrun of 69.8%. The expenditure incurred on these projects till January, 2020 is Rs. 12886.86 crore, which is 47.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

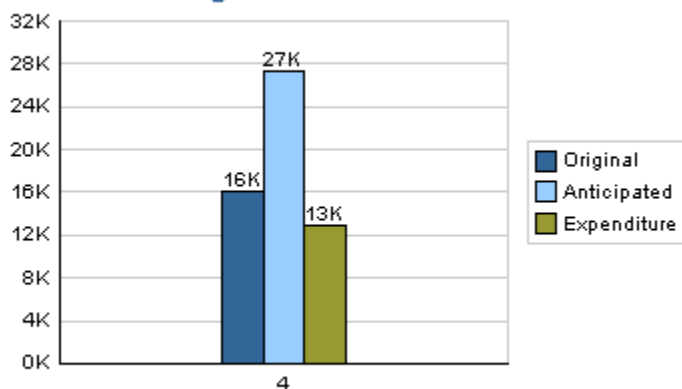

Sector wise current status of projects on the Flash Report


SHIPPING AND PORTS

Current Status:

Number of Projects	1
Number of Projects On Schedule	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 1 project, 1 project is on schedule

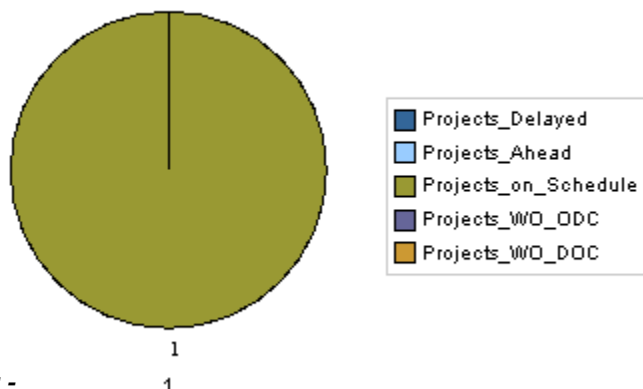


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 4200 crore but this was subsequently anticipated to Rs. 5369.18 crore implying a cost overrun of 27.8%. The expenditure incurred on these projects till January, 2020 is Rs. 1540.69 crore, which is 28.7% of the anticipated cost of the projects.

Figures are in Rs. Crore

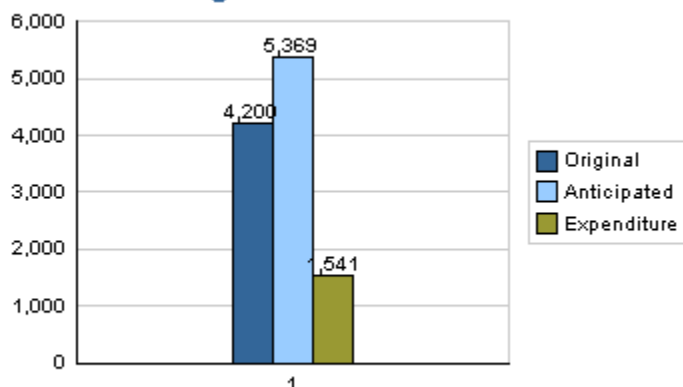

Sector wise current status of projects on the Flash Report


ROAD TRANSPORT AND HIGHWAYS

Current Status:

Number of Projects	867
Number of Projects On Schedule	59
Number of Projects Delayed	186
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	96
Number of Projects Without Date Of Commissioning	525

Brief Analysis

Project Status with respect to Original Schedule: Out of 867 projects, 1 project is ahead of schedule, 59 projects are on schedule 186 projects are delayed. 525 projects do not have fixed dates of commissioning. 96 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

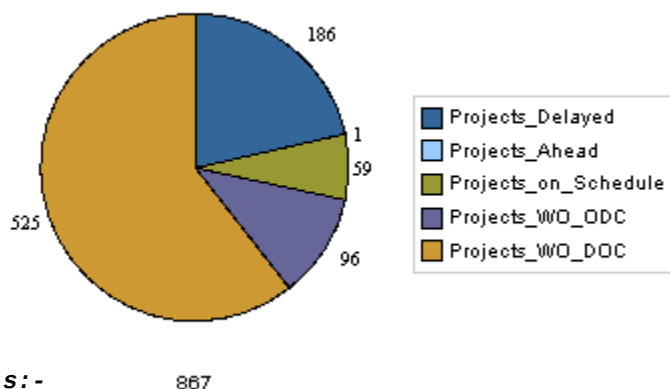


Total No Of Project's:-

867

Investment Scenario

Total original cost of implementation of 867 projects when sanctioned, was of the order of Rs. 513537.42 crore but this was subsequently anticipated to Rs. 528085.9 crore implying a cost overrun of 2.8%. The expenditure incurred on these projects till January, 2020 is Rs. 300798.25 crore, which is 57% of the anticipated cost of the projects.

Figures are in Rs. Crore

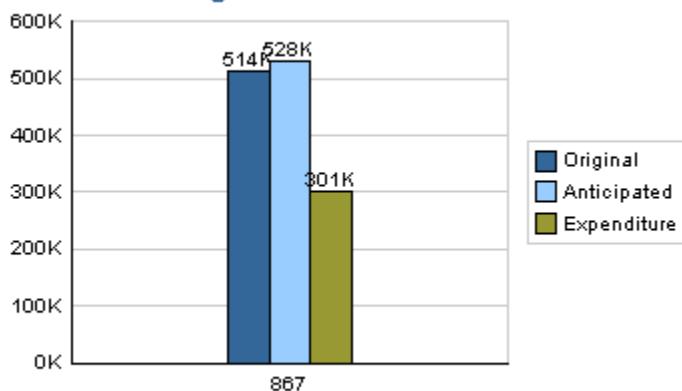

Sector wise current status of projects on the Flash Report


RAILWAYS

Current Status:

Number of Projects	312
Number of Projects On Schedule	35
Number of Projects Delayed	148
Number of Projects Ahead	6
Number of Projects Without Original Date of Commissioning	48
Number of Projects Without Date Of Commissioning	75

Brief Analysis

Project Status with respect to Original Schedule: Out of 312 projects, 6 projects are ahead of schedule, 35 projects are on schedule 148 projects are delayed. 75 projects do not have fixed dates of commissioning. 48 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

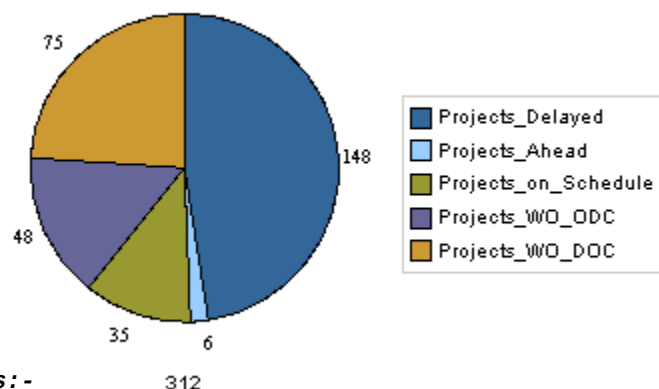


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 312 projects when sanctioned, was of the order of Rs. 459394.75 crore but this was subsequently anticipated to Rs. 671692.95 crore implying a cost overrun of 46.2%. The expenditure incurred on these projects till January, 2020 is Rs. 206153.91 crore, which is 30.7% of the anticipated cost of the projects.

Figures are in Rs. Crore

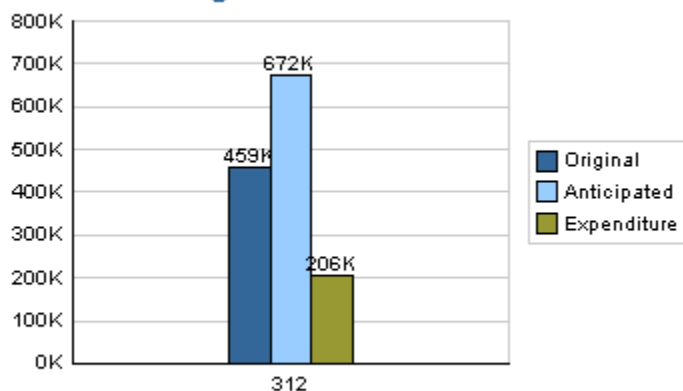

Sector wise current status of projects on the Flash Report

HEALTH AND FAMILY WELFARE


Current Status:

Number of Projects	23
Number of Projects On Schedule	3
Number of Projects Delayed	11

Number of Projects Without Original Date of Commissioning	6
Number of Projects Without Date Of Commissioning	3

Brief Analysis

Project Status with respect to Original Schedule: Out of 23 projects, 3 projects are on schedule 11 projects are delayed. 3 projects do not have fixed dates of commissioning. 6 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

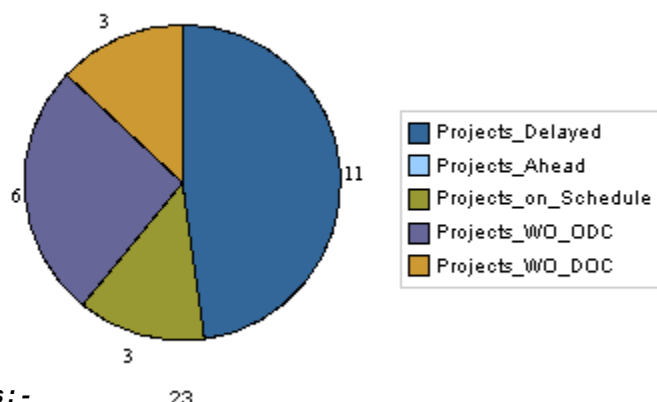


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 23 projects when sanctioned, was of the order of Rs. 12454.56 crore but this was subsequently anticipated to Rs. 12796.11 crore implying a cost overrun of 2.7%. The expenditure incurred on these projects till January, 2020 is Rs. 5325.26 crore, which is 41.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

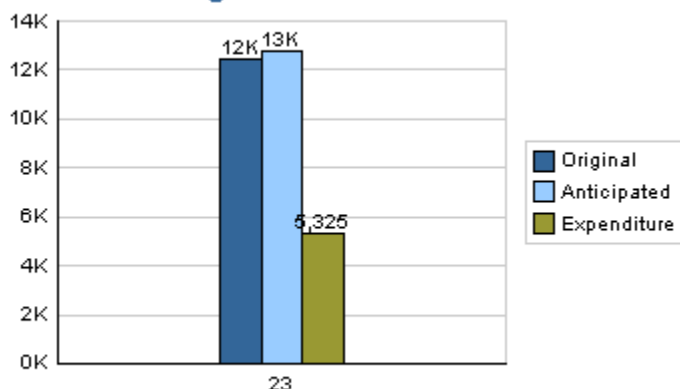

Sector wise current status of projects on the Flash Report


HEAVY INDUSTRY

Current Status:

Number of Projects	1
Number of Projects Delayed	1

Brief Analysis


Project Status with respect to Original Schedule: Out of 1 project, 1 project is delayed.



Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 1554 crore but this was subsequently anticipated to Rs. 1554 crore. The expenditure incurred on these projects till January, 2020 is Rs. 716.25 crore, which is 46.1% of the anticipated cost of the projects.

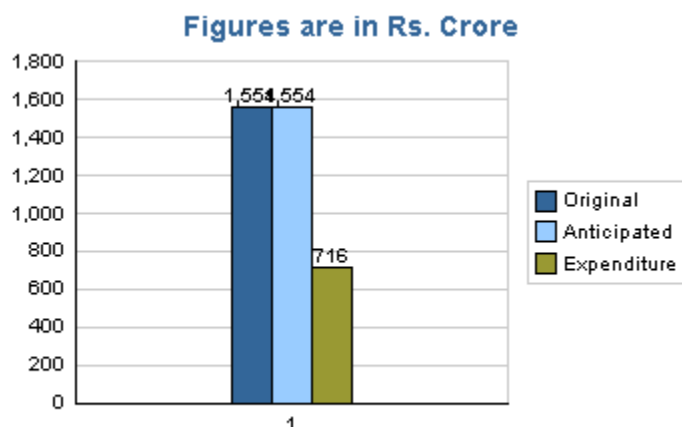

Sector wise current status of projects on the Flash Report

POWER


Current Status:

Number of Projects	64
Number of Projects On Schedule	10
Number of Projects Delayed	48

Number of Projects Without Date Of Commissioning	6
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 64 projects, 10 projects are on schedule 48 projects are delayed. 6 projects do not have fixed dates of commissioning.

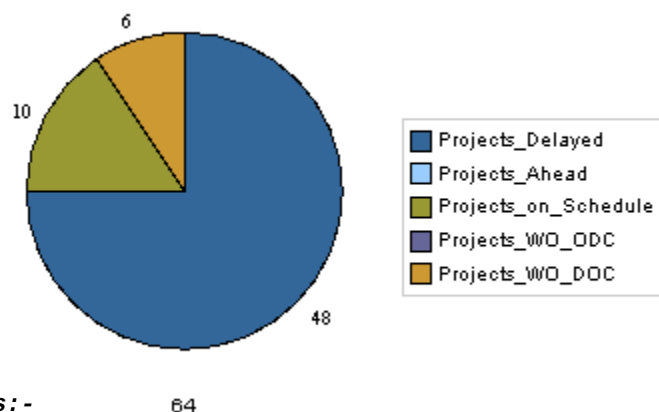


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 64 projects when sanctioned, was of the order of Rs. 273781.33 crore but this was subsequently anticipated to Rs. 344106.51 crore implying a cost overrun of 25.7%. The expenditure incurred on these projects till January, 2020 is Rs. 222894.97 crore, which is 64.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

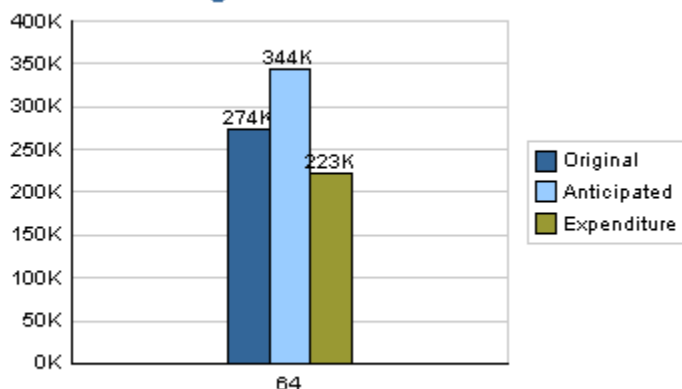

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	148
Number of Projects On Schedule	69
Number of Projects Delayed	60
Number of Projects Ahead	7
Number of Projects Without Original Date of Commissioning	2
Number of Projects Without Date Of Commissioning	10

Brief Analysis

Project Status with respect to Original Schedule: Out of 148 projects, 7 projects are ahead of schedule, 69 projects are on schedule 60 projects are delayed. 10 projects do not have fixed dates of commissioning. 2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

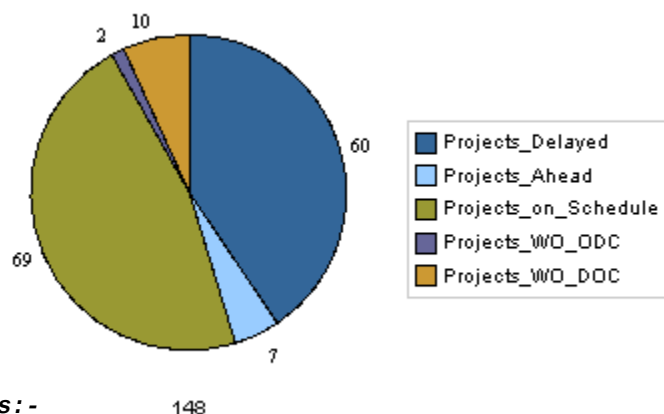


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 148 projects when sanctioned, was of the order of Rs. 269889.88 crore but this was subsequently anticipated to Rs. 284938.4 crore implying a cost overrun of 5.6%. The expenditure incurred on these projects till January, 2020 is Rs. 101562.39 crore, which is 35.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

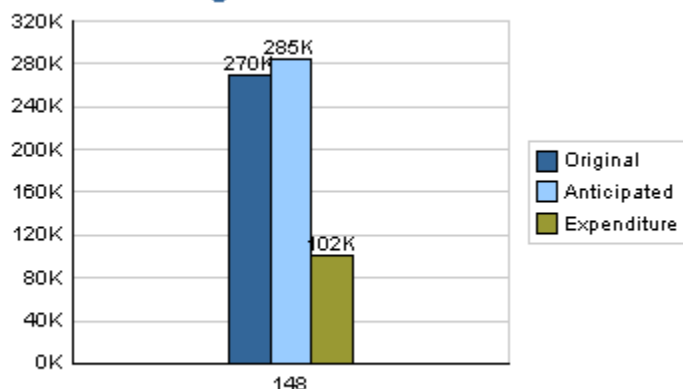

Sector wise current status of projects on the Flash Report


STEEL

Current Status:

Number of Projects	9
Number of Projects On Schedule	1
Number of Projects Delayed	8

Brief Analysis

Project Status with respect to Original Schedule: Out of 9 projects, 1 project is on schedule 8 projects are delayed.

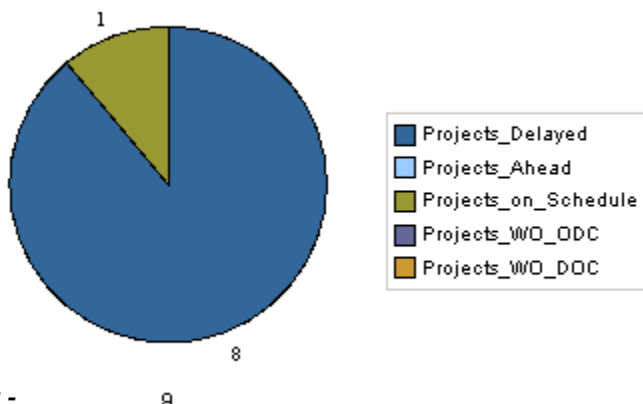


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 9 projects when sanctioned, was of the order of Rs. 26228.23 crore but this was subsequently anticipated to Rs. 33485.23 crore implying a cost overrun of 27.7%. The expenditure incurred on these projects till January, 2020 is Rs. 24413.37 crore, which is 72.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

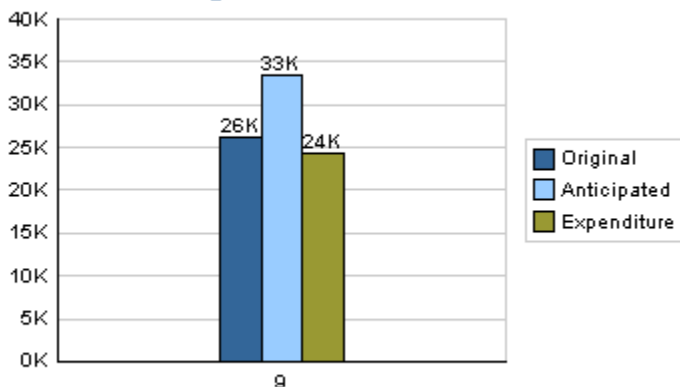

Sector wise current status of projects on the Flash Report


MINES

Current Status:

Number of Projects	5
Number of Projects On Schedule	3
Number of Projects Delayed	2

Brief Analysis

Project Status with respect to Original Schedule: Out of 5 projects, 3 projects are on schedule 2 projects are delayed.

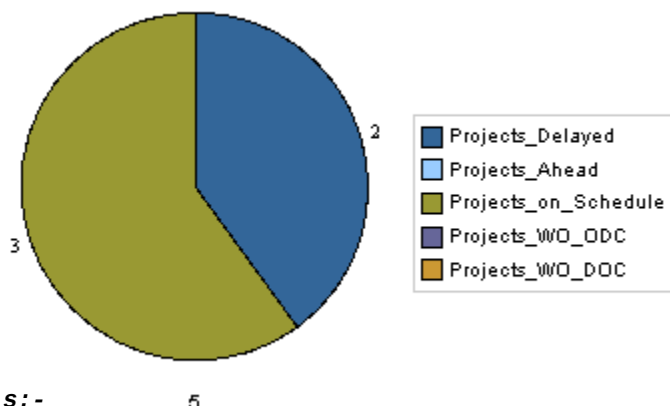


Total No Of Project's:-

5

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 7078.62 crore but this was subsequently anticipated to Rs. 7075.17 crore. The expenditure incurred on these projects till January, 2020 is Rs. 673.31 crore, which is 9.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

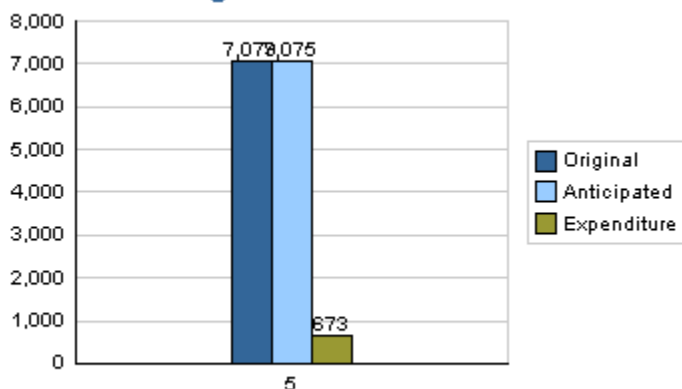

Sector wise current status of projects on the Flash Report

FERTILISERS


Current Status:

Number of Projects	4
Number of Projects On Schedule	1
Number of Projects Delayed	2

Number of Projects Without Date Of Commissioning	1
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 1 project is on schedule 2 projects are delayed. 1 project does not have fixed dates of commissioning.

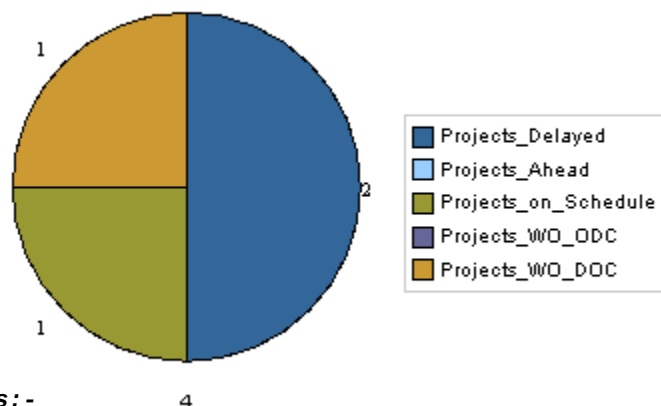

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 1101.28 crore but this was subsequently anticipated to Rs. 1101.28 crore. The expenditure incurred on these projects till January, 2020 is Rs. 701.67 crore, which is 63.7% of the anticipated cost of the projects.

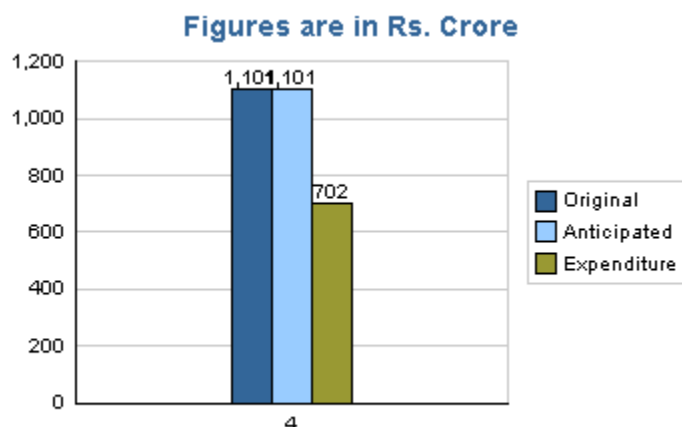

Sector wise current status of projects on the Flash Report

COAL


Current Status:

Number of Projects	107
Number of Projects On Schedule	54
Number of Projects Delayed	39

Number of Projects Without Original Date of Commissioning	3
Number of Projects Without Date Of Commissioning	11

Brief Analysis

Project Status with respect to Original Schedule: Out of 107 projects, 54 projects are on schedule 39 projects are delayed. 11 projects do not have fixed dates of commissioning. 3 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

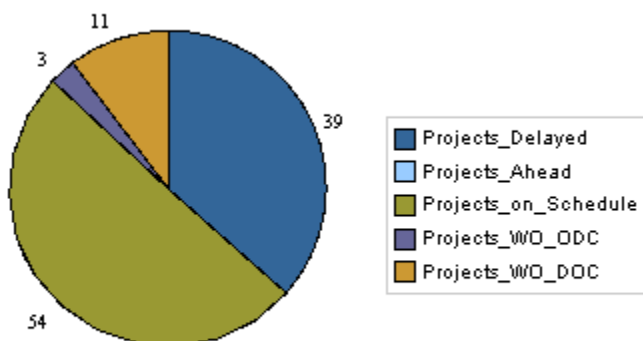


Total No Of Project's:-

107

Investment Scenario

Total original cost of implementation of 107 projects when sanctioned, was of the order of Rs. 104637.11 crore but this was subsequently anticipated to Rs. 108558.02 crore implying a cost overrun of 3.7%. The expenditure incurred on these projects till January, 2020 is Rs. 38613.72 crore, which is 35.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

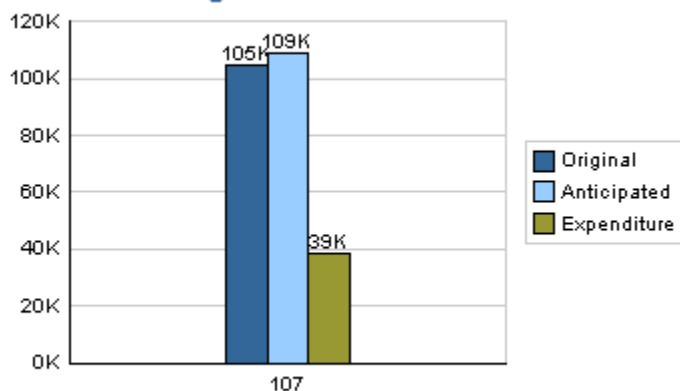

Sector wise current status of projects on the Flash Report

CIVIL AVIATION


Current Status:

Number of Projects	13
Number of Projects On Schedule	8
Number of Projects Delayed	4

Number of Projects Without Date Of Commissioning	1
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 13 projects, 8 projects are on schedule 4 projects are delayed. 1 project does not have fixed dates of commissioning.

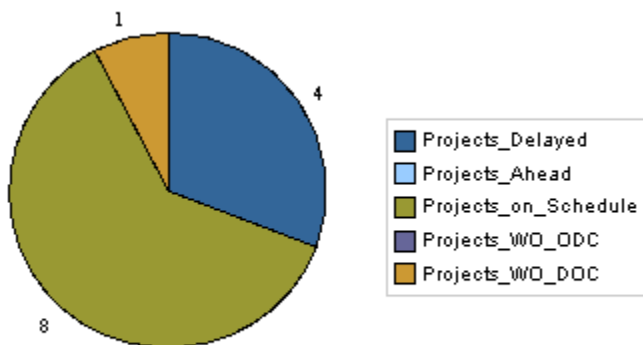


Total No Of Project's:-

13

Investment Scenario

Total original cost of implementation of 13 projects when sanctioned, was of the order of Rs. 8607.51 crore but this was subsequently anticipated to Rs. 8734.44 crore implying a cost overrun of 1.5%. The expenditure incurred on these projects till January, 2020 is Rs. 1357.47 crore, which is 15.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

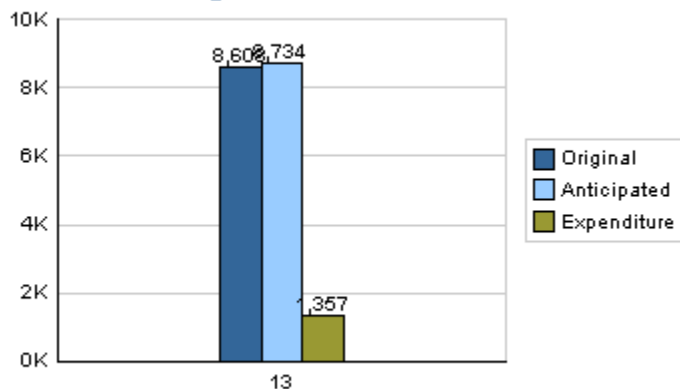

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	4

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed.



Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 67120 crore but this was subsequently anticipated to Rs. 80348 crore implying a cost overrun of 19.7%. The expenditure incurred on these projects till January, 2020 is Rs. 50215.38 crore, which is 62.5% of the anticipated cost of the projects.

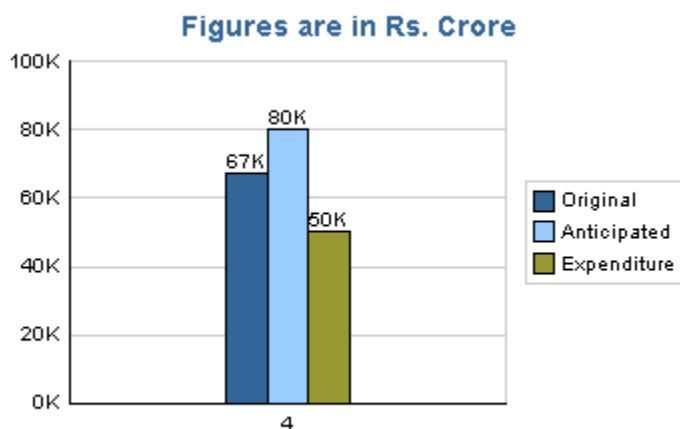

Annexure - I

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE (JANUARY 2020)

(All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	A & N ISLANDS	9	2,786.01	2,893.59	469.97
2	ANDHRA PRADESH	74	1,18,849.8	1,74,097.08	70,898.33
3	ARUNACHAL PRADESH	40	21,795.08	40,754.39	24,881.93
4	ASSAM	46	45,966.37	50,592	13,558.79
5	BIHAR	104	92,846.83	1,28,093.38	65,903.63
6	CHANDIGARH	2	349.15	570	0
7	CHHATISGARH	43	77,690.97	89,413.27	47,605.9
8	D & N HAVELI	1	6,086.08	5,842.31	4,784.88
9	DELHI	34	89,958.97	91,744.92	45,835.28
10	GOA	11	5,629.77	5,640.26	1,827.19
11	GUJARAT	59	87,567.29	93,803.49	49,392.11
12	HARYANA	43	34,582.59	38,034.22	18,035.79
13	HIMACHAL PRADESH	13	18,162.17	28,392.7	14,600.01
14	JAMMU AND KASHMIR	16	20,520.64	46,447.89	36,041.31
15	JHARKHAND	48	62,232.07	67,540.06	28,937.9
16	KARNATAKA	64	73,464.28	77,159.37	22,599.95
17	KERALA	20	36,309.6	40,285.87	16,003.04
18	MADHYA PRADESH	80	87,338.98	95,538.3	47,687.03
19	MAHARASHTRA	252	2,33,558.29	2,44,633.94	1,06,877.61
20	MANIPUR	5	6,002.36	14,012.39	9,885.31
21	MEGHALAYA	7	3,245.09	8,481.17	1,300.14
22	MIZORAM	13	7,757.62	11,189.69	4,941.79
23	MULTI STATE	126	3,57,261.72	4,70,314.27	1,49,561.72
24	NAGALAND	26	14,842.43	17,765.36	2,239.74
25	ODISHA	91	1,04,396.42	1,06,834.86	45,626.97
26	PONDICHERRY	1	195	195	0
27	PUNJAB	27	13,539.35	15,632.85	9,819.43
28	RAJASTHAN	61	45,605.93	53,170.39	35,960.93
29	SIKKIM	9	3,476.73	6,368.17	1,209.79
30	TAMIL NADU	64	1,14,330.18	1,32,336.42	70,691.55
31	TELANGANA	55	39,236.69	41,702.69	15,630.49
32	TRIPURA	7	1,977.29	2,159.55	1,156.43
33	UTTAR PRADESH	132	1,51,011.3	1,57,228.23	77,459
34	UTTARAKHAND	32	34,435.7	39,959.77	12,846.32
35	WEST BENGAL	77	62,203.95	79,188.6	43,334.38
TOTAL		1,692	20,75,212.7	24,78,016.45	10,97,604.64

List of Projects in which Expenditure is More than Approved Cost

Annexure - II

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	9/2003	3,492.00 -	6,840.00	5,862.38	09/2010 09/2016	10/2021
	<u>Nuclear Power Corporation Of India Limited</u>						
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	14,629.00	12/2015 -	09/2021
	Total		14,951.00 -	23,420.00	20,491.38		
	<u>COAL</u>						
	<u>Mahanadi Coal Fields Limited</u>						
3	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]	12/2007	457.77 -	457.77	568.14	03/2013 -	03/2022
4	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]	8/2008	207.28 -	207.28	306.94	03/2012 -	03/2021
5	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.10 -	490.10	524.33	03/2017 -	03/2021
6	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]	12/2007	172.08 -	172.08	377.07	03/2010 -	03/2022
	<u>Singareni Colliers Company Limited</u>						
7	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	326.69	03/2012 -	03/2024
	Total		1,576.26 -	1,776.09	2,103.17		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation Ltd</u>						
8	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 -	270.00	210.75	05/2017 -	06/2020
9	AIIMS - OPD(NEW) - [N21000009]	8/2014	293.65 -	325.00	304.62	05/2017 -	01/2020
10	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]	12/2014	168.90 -	191.20	169.51	05/2017 -	07/2019
11	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	9/2014	505.58 -	585.00	586.96	03/2018 -	09/2019
	Total		1,172.57 -	1,371.20	1,271.84		
	<u>PETROLEUM</u>						
	<u>Indian Oil Corporation Limited</u>						
12	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]	5/2016	664.00 -	729.40	664.73	12/2020 -	02/2020

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Indian Strategic Petroleum Reserves Ltd</u>						
13	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	1/2006	993.00 -	1,693.00	1,549.85	01/2012 -	-
	<u>Oil & Natural Gas Corporation Limited</u>						
14	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	3/2011	861.79 -	1,683.06	1,386.15	05/2013 02/2020	02/2020
	Total		2,518.79 -	4,105.46	3,600.73		
	<u>POWER</u>						
	<u>National Hydro-Electric Power Corporation</u>						
15	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	9/2002	3,919.59 -	9,997.11	7,761.19	09/2009 12/2021	12/2021
16	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	9/2003	6,285.33 -	19,496.34	11,842.12	09/2010 08/2023	08/2023
	<u>National Thermal Power Corporation</u>						
17	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	12,865.92	12,503.29	01/2018 03/2020	03/2020
18	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]	4/2012	9,750.89 -	12,176.28	10,103.00	02/2017 06/2020	06/2020
19	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	1/2007	5,353.00 -	9,583.00	8,056.25	07/2012 -	09/2020
20	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	12,826.56	10/2017 03/2020	03/2020
	Total		48,793.36 -	76,858.47	63,092.41		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
21	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	4/2011	184.06 -	312.00	293.06	03/2019 03/2020	03/2020
22	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	2/1997	2,271.50 -	4,517.49	2,495.07	03/2021 -	03/2022
	<u>East Central Railways</u>						
23	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]	3/1999	1,033.07 -	3,376.00	3,349.65	- -	03/2021
24	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	4/1997	324.73 -	1,050.00	1,041.96	03/2012 -	03/2020
25	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]	4/1991	329.39 -	1,483.14	1,060.33	- -	12/2021
26	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	4/2013	213.01 -	440.00	432.20	- -	01/2020
	<u>East Coast Railway</u>						
27	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	3/2012	155.81 -	238.03	205.65	03/2020 -	03/2021

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Eastern Railways</u>						
28	DEOGHAR - SULTANGANJ (INL), ER - [N220100273]	4/2000	607.09 -	1,425.44	637.56	02/2013 -	03/2024
29	PIRPAINTI-BHAGALPUR - [N22000222]	4/2011	261.38 -	492.84	492.84	- -	05/2019
30	BANDEL-BOINCHI 3RD LINE - [N22000221]	4/2011	288.35 -	402.48	402.48	- -	03/2020
31	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]	4/2011	175.80 -	260.83	260.83	- -	03/2021
32	MONIGRAM- NIMTITA - [N22000301]	4/2012	250.93 -	310.70	287.10	- -	03/2024
	<u>Metropolitan Rapid Transport Projects</u>						
33	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [N220100268]	3/2000	1,049.69 -	3,404.92	3,837.57	12/2006 -	-
34	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	3/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021
	<u>North Central Railway</u>						
35	ETAWAH-MAINPURI (NL),NCR - [N220100318]	4/1997	120.00 -	346.00	345.51	12/2008 -	-
	<u>North East Frontier Railway</u>						
36	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [N220100266]	4/2000	1,180.19 -	4,541.00	3,346.08	12/2008 -	03/2021
37	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]	2/1999	380.60 -	1,871.00	1,087.60	04/2010 -	-
38	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	4/2011	314.00 -	728.00	731.27	03/2019 -	03/2020
39	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	4/2010	241.52 -	373.87	273.20	- -	06/2021
40	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	4/1999	819.23 -	1,871.00	1,082.01	- -	-
	<u>North Eastern Railway</u>						
41	HATHUA-BHATNI (N L) (NER) - [N220100319]	4/2005	230.03 -	230.03	277.14	12/2022 -	12/2022
42	CHHAPRA-BALLIA UP - [N22000134]	3/2013	295.00 -	477.31	370.93	01/2019 -	01/2020
	<u>North Western Railway</u>						
43	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	4/2012	246.08 -	348.55	248.71	12/2019 -	02/2021
44	AJMER-BANGURGRAM - [N22000155]	4/2011	213.39 -	303.56	285.01	11/2019 -	12/2020
45	ALWAR-BANDIKUI DOUBLING - [N22000157]	4/2013	242.09 -	410.00	381.92	02/2019 -	02/2020
	<u>Northern Railway</u>						
46	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]	4/2007	336.91 -	791.39	517.05	- -	03/2022

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
47	HARIDWAR-LAKSAR - [N22000289]	4/2012	219.83 -	346.63	233.23	- -	06/2020
48	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	3/2002	625.00 -	859.00	835.35	03/2016 -	03/2021
	<u>Rail Vikas Nigam Ltd.</u>						
49	HARIDASPUR-PARADEEP(NL) - [220100285]	4/1996	1,185.64 -	1,844.47	1,883.44	12/2017 -	03/2020
50	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	4/2000	133.41 207.00	396.00	388.21	03/2009 03/2009	06/2020
51	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	3/2012	1,183.25 -	1,183.25	1,184.32	12/2020 -	12/2022
52	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	3/2009	942.95 -	1,120.00	1,046.08	03/2019 -	06/2022
53	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	3/2006	948.04 -	1,500.00	1,451.81	03/2020 -	03/2021
54	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	3/2009	713.48 -	2,300.00	2,131.56	03/2020 -	03/2021
55	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	4/2011	927.01 -	1,200.00	1,209.55	03/2019 -	03/2020
56	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	4/2012	632.68 -	816.55	720.70	03/2016 -	12/2020
57	AHMEDABAD-BOTAD (GC) - [N22000140]	4/2012	975.62 -	1,082.32	1,202.24	12/2021 -	12/2021
58	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]	3/2012	1,503.71 -	2,200.00	1,966.03	03/2020 -	03/2022
	<u>South Central Railway</u>						
59	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	3/1996	164.36 -	1,050.00	999.64	02/2009 -	-
60	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	4/2017	119.73 185.00	449.39	298.13	03/2022 -	12/2022
	<u>South Eastern Railway</u>						
61	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	4/2012	148.77 -	377.00	183.96	12/2016 08/2018	03/2020
	<u>Southern Railway</u>						
62	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI - [N22000079]	9/2007	724.69 -	2,072.50	1,471.60	02/2019 -	02/2020
63	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	4/2011	120.70 -	1,800.00	187.92	03/2019 -	12/2019
64	MADURAI-BODINAYAKKANUR - [N22000201]	4/2008	164.41 -	450.00	197.11	- -	03/2020
65	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	9/1995	303.98 -	980.00	683.11	03/2020 -	03/2021
66	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]	2/1999	257.00 257.00	257.00	268.31	03/2018 -	-
67	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	2/1996	268.87 -	950.00	927.86	03/2005 -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
68	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187	4/1999	198.68 -	556.64	305.22	- -	-
69	KURUPPANTHARA-CHINGAVANAM - [N22000190	4/2007	270.14 -	457.08	373.51	- -	-
	<u>West Central Railway</u>						
70	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314	4/2001	424.60 -	2,909.99	1,975.34	03/2021 -	03/2023
71	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	9/1998	247.66 -	8,248.50	1,986.78	05/2008 -	03/2023
	<u>Western Railway</u>						
72	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125	4/2006	117.36 196.95	202.35	809.40	03/2011 -	03/2017
73	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121	4/2008	829.74 -	1,310.23	1,532.69	03/2020 03/2021	03/2021
	Total		30,989.74 -	75,499.45	56,088.55		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
74	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306	11/2010	624.41 -	992.67	886.01	03/2011 12/2020	12/2020
75	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314	1/2013	182.28 -	269.14	185.49	02/2013 -	12/2019
76	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388	11/2013	497.05 -	881.05	624.54	05/2017 -	05/2020
77	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415	8/2010	195.04 -	377.99	312.41	10/2010 12/2020	06/2020
78	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523	12/2011	159.39 -	159.39	210.29	11/2017 -	-
79	CITTORGARH-NEEMACH (4L) OF NH-79 AND NIMBAHARA PRATAPGARH (2L+PS) OF NH-113 UNDER PPP. - [N24000955	10/2012	511.21 -	511.21	814.79	10/2013 -	-
80	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181	8/2010	186.96 -	305.61	279.13	09/2014 06/2020	06/2020
81	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938	3/2018	297.12 294.00	294.12	373.98	07/2018 01/2020	01/2020
82	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467	9/2012	511.00 -	511.00	2,323.04	10/2013 -	-
83	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411	11/2014	218.31 -	307.47	263.85	02/2018 -	-
84	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371	10/2013	445.89 -	653.29	464.05	03/2017 -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
85	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]	8/2010	193.69 -	327.92	258.71	10/2010 06/2021	06/2021
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
86	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]	10/2015	179.82 -	179.82	197.77	01/2019 -	-
	<u>National Highways Authority Of India</u>						
87	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]	12/2003	160.00 -	167.98	223.81	05/2008 -	06/2019
88	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61 -	360.84	454.21	04/2010 -	07/2019
89	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	3/2017	988.34 -	1,043.28	1,035.00	03/2020 -	08/2020
90	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]	1/2017	244.90 -	244.90	251.87	05/2019 -	12/2019
91	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]	11/2012	605.84 -	722.46	722.46	07/2018 12/2019	02/2020
92	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]	10/2016	447.75 -	447.75	1,028.99	- -	08/2020
93	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]	9/2016	1,244.10 -	1,244.10	1,445.00	- -	02/2020
94	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]	9/2016	950.69 -	1,108.00	1,399.33	08/2019 -	12/2020
95	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]	9/2016	1,239.82 -	1,239.82	1,427.14	- -	05/2020
96	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]	8/2016	248.97 -	248.97	249.15	05/2019 -	03/2020
97	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]	12/2015	479.20 -	479.20	712.89	05/2018 03/2018	10/2019
98	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]	4/2014	1,665.00 -	1,665.00	4,357.89	- -	-
99	FOUR LANING FROM MPMHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]	4/2010	1,170.52 -	1,170.52	2,051.36	06/2012 -	-
100	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]	7/2015	1,871.34 -	1,871.34	3,544.79	01/2018 12/2018	03/2020
101	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]	6/2015	1,583.79 -	1,583.79	1,648.90	01/2019 10/2019	10/2019
102	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	5/2013	1,055.00 -	1,601.77	1,393.40	11/2015 -	-
103	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]	2/2008	1,673.70 -	1,673.70	3,326.93	10/2011 -	-
104	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]	12/2015	1,083.00 -	1,083.00	1,487.87	06/2018 -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
105	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462	5/2014	1,655.01 -	1,655.01	1,867.51	08/2016 -	12/2020
106	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544	3/2016	676.73 -	676.73	945.17	04/2019 -	-
107	TRICHY - KARUR - [N24000528	3/2007	516.00 -	516.00	886.96	07/2008 -	-
108	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520	8/2015	275.90 -	275.90	289.13	- 02/2016	10/2019
109	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518	8/2015	399.54 -	297.27	509.75	04/2019 -	-
110	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224	10/2012	1,928.22 -	2,945.00	2,467.00	04/2015 01/2017	06/2020
111	AHMEDABAD TO VADODARA SECTION - [N24000222	1/2013	2,125.24 -	2,125.24	4,669.71	12/2015 -	-
112	ETAWAH CHAKERI - [N24000219	3/2013	1,573.00 -	1,573.00	2,078.25	09/2015 -	-
113	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208	7/2012	291.36 -	291.36	459.07	01/2014 -	-
114	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206	4/2012	1,396.18 -	1,396.18	2,894.94	09/2014 -	03/2020
115	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205	12/2011	1,047.00 -	1,047.00	1,874.43	06/2014 -	03/2019
116	4-LANING OF BRAHAMPORE-FARAKA - [N24000203	2/2011	998.79 -	998.79	1,822.59	08/2013 -	03/2021
117	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178	4/2011	571.00 -	571.00	582.53	10/2013 -	-
118	INDORE-JHABUA-GUJRAT/MP - [N24000136	10/2010	1,175.00 -	1,175.00	1,509.96	04/2013 -	-
119	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233	4/2014	1,266.60 -	1,544.00	1,446.45	09/2016 -	-
120	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232	11/2013	1,916.79 -	1,916.79	1,948.92	11/2016 -	-
121	NALBARI TO BIJNI (AS-6) - [N24000047	12/2003	225.00 -	225.00	328.47	06/2008 -	09/2019
122	NALBARI T BIJNI (AS-7) - [N24000048	12/2003	208.00 -	230.00	340.21	04/2008 -	03/2020
123	INDORE-DEWAS(NH-3) - [N24000159	11/2010	325.00 -	475.00	469.54	05/2013 -	-
124	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230	5/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	-
125	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149	2/2010	617.00 -	617.00	943.17	08/2012 -	12/2019
126	4-LANING OF FARAKA-RAIGANJ - [N24000202	2/2011	1,078.84 -	1,078.84	2,195.64	08/2013 -	05/2020
127	MUZAFFARNAGAR-HARIDWAR - [N24000201	9/2011	754.00 -	754.00	1,364.18	03/2013 11/2019	11/2020
128	PANIKHOLI-RIMOLI - [N24000197	3/2012	1,410.00 -	1,410.00	1,935.14	09/2014 -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
129	SRINAGAR TO BANIHAL - [N24000189]	6/2011	1,100.70 -	1,100.70	2,898.41	06/2014 09/2017	10/2020
130	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]	1/2011	575.00 -	575.00	850.24	07/2013 -	03/2020
131	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]	10/2011	375.09 -	375.09	494.33	04/2014 -	-
132	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]	9/2011	574.00 -	574.00	768.73	03/2014 -	-
133	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]	11/2011	1,535.00 -	1,535.00	3,260.65	05/2014 12/2019	03/2020
134	KANDLA - MUNDRA PORT - [N24000175]	1/2011	953.88 -	953.88	976.79	07/2013 11/2020	11/2020
135	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]	12/2015	611.65 -	611.65	728.24	06/2016 -	-
136	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]	6/2015	845.24 -	941.00	859.59	- -	01/2020
137	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]	1/2015	972.50 -	972.50	1,492.00	07/2017 12/2019	03/2020
138	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]	7/2015	1,657.20 -	1,657.20	2,345.00	01/2019 -	-
139	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]	8/2014	822.90 -	822.90	844.08	04/2018 -	-
140	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]	9/2015	414.51 -	414.00	543.46	05/2018 05/2020	05/2020
141	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]	11/2012	530.07 -	530.07	556.02	08/2016 -	06/2020
142	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]	4/2014	495.78 -	495.78	633.24	01/2016 -	-
143	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]	4/2014	351.34 -	351.34	433.68	01/2016 -	-
144	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]	9/2011	1,250.00 -	1,250.00	1,336.07	12/2013 -	06/2020
145	GHAZIABAD-ALIGARH NH-91 - [N24000170]	2/2011	1,141.00 -	1,141.00	1,715.42	08/2013 -	-
146	PATNA-MUZZAFFARPUR - [N24000165]	8/2010	671.30 -	671.30	1,132.48	02/2013 -	03/2020
147	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]	7/2010	1,813.76 -	1,813.76	2,393.99	07/2013 -	-
148	NASHRI- CHANANI - [N24000162]	5/2011	2,159.00 -	2,519.00	4,707.04	06/2015 -	-
149	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]	7/2010	1,987.00 -	1,987.00	2,913.83	07/2015 12/2019	09/2020
150	4 LANING OF NAGPUR-BETUL - [N24000155]	2/2011	2,498.76 -	2,498.76	2,531.46	08/2014 -	-
151	PUNE-SATARA(NH-4) - [N24000156]	10/2010	1,724.55 -	1,724.55	2,442.58	03/2013 -	03/2020

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
152	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	5/2009	1,108.00 -	2,967.50	3,990.72	11/2011 -	03/2020
	Total		71,078.37 -	77,352.39	1,10,424.72		
	<u>STEEL</u>						
	<u>Steel Authority Of India Limited (Sail)</u>						
153	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]	4/2015	3,127.30 -	3,127.30	3,201.42	04/2018 01/2020	01/2020
	Total		3,127.30 -	3,127.30	3,201.42		
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
154	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]	2/2014	156.57 -	156.57	159.35	08/2016 -	01/2020
	<u>Chennai Metro Rail Ltd</u>						
155	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]	2/2009	14,600.00 -	19,058.00	16,352.87	12/2015 -	-
	<u>Hindustan Steelwork Construction Limited</u>						
156	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]	5/2005	768.88 1,070.97	1,113.34	1,085.64	02/2014 -	-
157	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	3/2007	149.73 173.00	175.94	176.65	12/2015 -	-
	<u>Kochi Metro Rail Corporation Ltd</u>						
158	KOCHI METRO RAIL PROJECT - [N28000081]	7/2012	5,181.79 -	6,218.14	5,817.11	07/2017 -	03/2020
	Total		20,856.97 -	26,721.99	23,591.62		
	Grand Total		1,95,064.36	2,90,232.35	2,83,865.84		

Details of Projects Ahead of Schedule w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>FERTILISERS</u>						
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
1	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]	4/2018	426.72 -	426.72	268.46	04/2020 07/2020	04/2020
	Total		426.72 -	426.72	268.46		
	<u>PETROLEUM</u>						
	<u>Indian Oil Corporation Limited</u>						
2	PARADIP HYDERABAD PIPELINE - [N16000194]	1/2015	2,321.00 3,338.00	3,338.00	2,123.21	12/2020 -	08/2020
3	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]	5/2016	664.00 -	729.40	664.73	12/2020 -	02/2020
4	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]	8/2017	384.58	384.58	134.67	04/2021 -	09/2020
5	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]	9/2015	324.00 -	324.00	199.72	06/2020 -	03/2020
6	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]	3/2018	3,712.00 -	3,696.00	1,001.53	09/2022 -	06/2021
7	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]	8/2017	315.00 -	315.00	124.98	12/2021 -	12/2020
	Total		7,720.58 -	8,786.98	4,248.84		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
8	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	1/2013	12,964.60 17,304.00	17,304.00	14,367.00	05/2018 12/2021	06/2021
	<u>Power Grid Corporation Of India Limited</u>						
9	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 546.36	546.36	470.71	11/2016 06/2020	03/2020
10	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/- [N18000242]	2/2017	322.30 -	322.30	166.84	02/2019 04/2020	03/2020
	Total		13,809.19 -	18,172.66	15,004.55		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
11	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	2/2015	3,627.47 -	3,627.47	854.93	03/2024 -	03/2023
	<u>East Central Railways</u>						

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
12	GARHWA ROAD-RAMNA - [N22000465]	3/2015	348.23 -	348.23	211.06	03/2021 -	12/2020
	<u>North East Frontier Railway</u>						
13	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	4/2015	2,232.32 -	2,182.00	765.94	03/2022 -	03/2020
14	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	4/2016	602.27 -	612.00	344.08	12/2021 -	03/2020
	<u>Rail Vikas Nigam Ltd.</u>						
15	BHANUPALI-BILASPUR BERI NL - [N22000273]	4/2008	2,966.99 -	7,000.00	472.83	12/2026 -	12/2025
16	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78 -	723.78	.19	12/2025 -	03/2025
	Total		10,501.06 -	14,493.48	2,649.03		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
17	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]	8/2010	195.04 -	377.99	312.41	10/2010 12/2020	06/2020
18	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]	1/2017	576.48 -	576.48	237.30	01/2018 12/2020	01/2020
	<u>National Highways Authority Of India</u>						
19	GWALIOR-JHANSI, NH-75 - [N24000089]	12/2003	604.00 364.59	364.59	237.64	12/2009 08/2020	03/2020
20	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]	3/2017	247.02 -	157.49	31.97	03/2020 02/2021	02/2020
	Total		1,622.54 -	1,476.55	819.32		
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
21	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]	10/2016	422.00 -	422.00	15.11	- 03/2021	12/2020
22	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]	11/2017	171.72	171.72	45.00	03/2020 11/2020	03/2020
	Total		593.72 -	593.72	60.11		
	Grand Total		34,673.81	43,950.11	23,050.31		

Details of On Schedule Projects w.r.t. Original Schedule

Annexure - IV

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]	12/2016	859.86 -	860.00	232.44	03/2021 -	03/2021
2	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN - [N04000085]	7/2018	353.27 -	353.27	114.29	09/2020 -	09/2020
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICATION - [N04000079]	3/2017	358.89 -	358.89	29.73	04/2021 -	04/2021
4	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AIRPORT - [N04000075]	8/2018	951.28 -	951.28	71.55	10/2021 -	10/2021
5	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	7/2018	323.19 -	323.19	10.14	09/2021 -	09/2021
6	CCS INTERNATIONAL AIRPORT, LUCKNOW - [N04000077]	6/2018	1,383.00 -	1,383.00	210.62	09/2021 -	09/2021
7	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA - [N04000081]	1/2019	264.99 -	264.99	0.42	11/2021 -	11/2021
8	CONSTRUCTION OF NEW DOMESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082]	5/2018	539.20 -	539.20	25.64	10/2022 -	10/2022
	Total		5,033.68 -	5,033.82	694.83		
	<u>COAL</u>						
	<u>Bharat Coking Coal Limited</u>						
9	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	5.38	03/2021 -	03/2021
	<u>Central Coal Fields Limited</u>						
10	NORTH URIMARI EXPANSION OCP - [N06000182]	3/2019	1,553.06 -	1,553.06	204.04	03/2023 -	03/2023
11	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	190.41	03/2020 -	03/2020
	<u>Eastern Coal Fields Limited</u>						
12	TILABONI UG MINE - [N06000172]	2/2019	916.62 -	916.62	-	03/2027 -	03/2027
13	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	318.97	03/2022 -	03/2022
14	CHITRA EAST (RCE) OCP - [N06000169]	8/2018	513.98 -	513.98	93.85	03/2024 -	03/2024
15	SIDULI MINE (OC AND UG) - [N06000165]	5/2018	535.18 -	535.18	0.19	03/2026 -	03/2026
16	PARASEA- BELBAID REORGANISATION UG MINE - [N06000185]	7/2019	826.42 -	826.42	-	03/2027 -	03/2027

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
17	NAKRAKONDA KUMARDIH B OCP - [N06000170]	8/2018	502.68 -	502.68	-	03/2029 -	03/2029
18	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	112.11	03/2022 -	03/2022
	<u>Mahanadi Coal Fields Limited</u>						
19	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	445.23	03/2021 -	03/2021
20	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]	11/2018	2,838.87 -	2,838.87	1,169.40	03/2029 -	03/2029
21	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	1,213.54	03/2026 -	03/2026
22	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]	5/2018	2,434.75 -	2,434.75	140.36	03/2027 -	03/2027
	<u>Neyveli Lignite Corporation</u>						
23	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	8,596.47	11/2021 -	11/2021
	<u>Northern Coal Fields Limited</u>						
24	SEMARIA OPENCAST PROJECT - [N06000176]	5/2019	396.58 -	396.58	-	03/2026 -	03/2026
25	BLOCK-B EXPANSION OPENCAST PROJECT - [N06000184]	7/2019	998.71 -	998.71	-	03/2023 -	03/2023
26	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]	5/2017	1,783.09 -	1,783.09	292.75	03/2021 -	03/2021
27	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]	11/2017	1,255.17 -	1,255.17	123.08	03/2022 -	03/2022
	<u>Singareni Colliers Company Limited</u>						
28	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]	12/2015	477.65 -	477.65	2.11	03/2020 -	03/2020
	<u>South-Eastern Coal Fields Limited</u>						
29	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]	3/2016	869.44 -	869.44	117.99	03/2021 -	03/2021
30	MALACHUA OPENCAST PROJECT - [N06000139]	10/2015	488.33 -	488.33	27.33	03/2023 -	03/2023
31	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	104.77	03/2021 -	03/2021
32	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	88.82	03/2020 -	03/2020
33	MAHAMAYA OPENCAST PROJECT - [N06000164]	5/2018	410.26 -	410.26	9.53	03/2026 -	03/2026
34	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	110.31	03/2022 -	03/2022
35	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	4.94	03/2023 -	03/2023
36	JHIRIA WEST OPENCAST PROJECT - [N06000166]	11/2018	389.97 -	389.97	-	03/2026 -	03/2026
37	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
38	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [N060100093]	6/2010	11,816.40 -	11,816.40	2,920.18	03/2023 03/2016	03/2023

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
39	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	6.58	03/2023 -	03/2023
40	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	81.59	03/2020 -	03/2020
41	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
42	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
43	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	75.96	03/2026 -	03/2026
44	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	2,358.32	03/2023 -	03/2023
45	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	48.13	03/2021 -	03/2021
	<u>Western Coal Fields Limited</u>						
46	VISHNUPURI UG TO OC MINE - [N06000178]	7/2018	195.57 -	195.57	2.94	03/2025 -	03/2025
47	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	263.81	03/2025 -	03/2025
48	UKNI DEEP OC - [N06000179]	11/2018	318.14 -	318.14	148.14	03/2021 -	03/2021
49	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]	2/2017	328.00 -	328.00	186.61	03/2021 -	03/2021
50	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	415.50	03/2020 -	03/2020
51	BELLORA-NAIGAON DEEP OC - [N06000180]	11/2018	252.71 -	252.71	58.07	03/2021 -	03/2021
52	SAONER I UG TO OC PHASE I - [N06000177]	11/2016	162.10 -	162.10	51.16	03/2022 -	03/2022
53	KOLAR PIMPRI EXTENSION OC - [N06000160]	3/2017	362.73 -	362.73	322.62	03/2020 -	03/2020
54	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]	7/2016	409.87 -	409.87	19.96	03/2022 -	03/2022
55	BHANEGAON OC - [N06000121]	2/2015	187.94 -	409.68	129.61	03/2023 -	03/2023
56	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	225.02	03/2021 -	03/2021
57	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	319.76	190.69	03/2022 -	03/2022
58	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	202.03	03/2020 -	03/2020
59	GANDHIGRAM UG MINE - [N06000183]	8/2019	414.16 -	414.16	0.50	03/2026 -	03/2026
60	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	120.69	03/2020 -	03/2020
61	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	218.63	03/2020 -	03/2020
62	DHANKASA UG (1.00 MTY) - [N06000155]	9/2016	458.07 -	458.07	22.46	03/2022 -	03/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		75,668.00 -	75,890.54	21,440.78		
	<u>FERTILISERS</u>						
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
63	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]	4/2018	426.72 -	426.72	268.46	04/2020 07/2020	04/2020
	Total		426.72 -	426.72	268.46		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Central Public Works Department</u>						
64	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR - [N21000029]	3/2019	1,404.00 -	1,404.00	-	09/2023 -	09/2023
65	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]	3/2019	1,577.00 -	1,828.00	-	09/2025 -	09/2025
	<u>National Building Construction Corporation Ltd</u>						
66	AIIMS BILASPUR - [N21000028]	4/2018	1,351.00 -	1,471.00	421.44	09/2021 -	09/2021
	Total		4,332.00 -	4,703.00	421.44		
	<u>HUMAN RESOURCE DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
67	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA. - [N42000002]	5/2019	303.90 -	303.90	-	03/2020 -	03/2020
	Total		303.90 -	303.90	.00		
	<u>MINES</u>						
	<u>National Aluminum Company Limited (Nalco)</u>						
68	UTKAL D AND E COAL BLOCK - [N10000011]	5/2016	534.00 -	534.00	320.63	01/2020 -	01/2020
69	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]	12/2015	355.00 -	355.00	85.98	11/2020 -	11/2020
70	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]	11/2017	483.00 -	483.00	0.48	04/2021 04/2021	04/2021
	Total		1,372.00 -	1,372.00	407.09		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
71	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]	11/2018	248.55 -	248.55	29.20	06/2022 -	06/2022
72	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]	10/2018	206.26 -	206.26	13.42	03/2021 -	03/2021
73	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364]	7/2017	580.20 -	580.20	66.56	02/2021 -	02/2021
74	2ND GENERATION LIGNOCELLULOIC BIOMASS ETHANOL BIOFUEL REFINERY AT BARGARH (ODISHA) - [N16000374]	8/2019	1,607.00 -	1,607.00	40.99	08/2022 -	08/2022
75	2G ETHANOL BIO REFINERY AT BARGARH - [N16000341]	8/2017	750.00 -	750.00	34.73	12/2020 -	12/2020
76	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]	2/2016	554.00 -	554.00	375.80	02/2020 -	02/2020
77	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]	9/2018	11,130.00 -	11,130.00	89.09	03/2023 -	03/2023
78	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL - [N16000365]	12/2017	1,524.06 -	1,524.06	22.01	12/2021 -	12/2021
79	PUNE POL STORAGE DEPOT - [N16000313]	8/2016	282.64 -	282.64	164.77	08/2020 -	08/2020
	<u>Gas Authority Of India Limited</u>						
80	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329]	10/2017	226.45 -	226.45	62.72	10/2022 -	10/2022
81	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]	7/2015	2,881.40 -	2,000.00	1,326.88	12/2020 -	12/2020
82	BARAUNI-GUWAHATI PIPELINE - [N16000334]	6/2018	3,308.00 -	3,308.00	1,433.56	12/2021 -	12/2021
83	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]	7/2017	182.20 -	182.20	34.88	07/2022 -	07/2022
84	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	287.49	138.25	04/2022 -	04/2022
85	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]	7/2017	243.53 -	243.53	58.94	07/2022 -	07/2022
86	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	2/2015	749.00 -	842.00	606.89	02/2020 -	02/2020
87	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]	9/2018	225.54 -	225.54	2.44	02/2021 -	02/2021
88	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR - [N16000330]	10/2017	221.45 -	221.45	52.67	10/2022 -	10/2022
89	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	3/2017	1,933.00 -	1,933.00	1,068.40	12/2020 -	12/2020
90	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]	10/2017	359.25 -	359.25	81.40	10/2022 -	10/2022
91	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	3/2017	1,740.00 -	1,740.00	612.62	12/2020 -	12/2020
92	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]	3/2017	3,437.00 -	3,437.00	1,326.48	12/2020 -	12/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
93	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]	3/2017	2,433.00 -	2,433.00	1,566.59	12/2020 -	12/2020
	<u>Hindustan Petroleum Corporation Limited</u>						
94	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	9/2017	2,677.00 -	2,677.00	1,106.90	03/2021 -	03/2021
95	SETTING UP OF PHASE II FACILITIES FOR HPCL GREEN R AND D CENTRE AT BENGALURU - [N16000380]	6/2018	380.00 -	380.00	82.70	11/2021 -	11/2021
96	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]	11/2017	255.00 -	255.00	128.36	11/2020 -	11/2020
97	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369]	12/2018	854.00 -	854.00	56.18	12/2022 -	12/2022
98	SWRO II WITH LLPH FACILITIES - [N16000378]	9/2019	196.26 -	196.26	-	07/2020 -	07/2020
99	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]	9/2015	4,199.00 -	5,060.00	3,446.40	03/2020 -	03/2020
100	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]	9/2016	1,879.00 -	1,879.00	1,590.22	06/2020 -	06/2020
101	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367]	6/2019	2,166.38 -	2,166.38	33.41	06/2022 -	06/2022
	<u>Indian Oil Corporation Limited</u>						
102	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]	4/2018	5,654.00 -	5,654.00	686.68	10/2021 -	10/2021
103	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]	3/2018	676.00 -	676.00	271.05	12/2021 -	12/2021
104	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT - [N16000363]	12/2018	278.60 -	278.60	-	06/2021 -	06/2021
105	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]	6/2019	371.00 -	371.00	-	09/2022 -	09/2022
106	LPG BP PROJECT CHITTOOR - [N16000381]	7/2019	167.00 -	167.00	3.62	07/2022 -	07/2022
107	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	1/2015	1,823.00 -	3,027.90	1,030.43	12/2020 -	12/2020
108	R and D CAMPUS II AT FARIDABAD - [N16000375]	6/2019	2,281.94 -	2,281.94	-	12/2022 -	12/2022
109	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	1,074.02	08/2021 -	08/2021
110	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]	5/2019	3,361.00 -	3,361.00	468.48	08/2021 -	08/2021
111	LPG BP PROJECT MOTIHARI - [N16000317]	5/2018	206.50 -	206.50	38.09	03/2021 -	03/2021
112	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]	5/2013	711.00 -	711.00	11.12	06/2020 -	06/2020
113	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]	11/2018	462.30 -	462.30	-	09/2021 -	09/2021
114	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]	10/2018	316.20 -	316.20	18.83	10/2021 -	10/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
115	LAB REVAMP AT GUJARAT REFINERY - [N16000377]	10/2019	403.00 -	403.00	43.50	12/2021 -	12/2021
116	AUGMENTATION OF CTMPL - [N16000286]	12/2016	228.00 -	228.00	36.09	06/2020 -	06/2020
117	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]	1/2015	342.00 -	342.00	-	03/2021 -	03/2021
118	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]	4/2016	1,021.00 -	1,021.00	4.45	12/2020 -	12/2020
119	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]	7/2018	189.00 -	189.00	33.25	01/2021 -	01/2021
120	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]	4/2018	522.00 -	522.00	187.36	03/2021 -	03/2021
121	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY - [N16000382]	11/2019	5,251.00 -	5,251.00	-	05/2023 -	05/2023
122	DEVELOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]	12/2017	199.36 -	199.36	9.39	10/2020 -	10/2020
123	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]	7/2014	247.00 -	247.00	-	03/2021 -	03/2021
124	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]	9/2016	208.35 -	208.35	148.25	07/2020 -	07/2020
125	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]	8/2018	1,636.00 -	1,636.00	160.86	08/2020 -	08/2020
126	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]	10/2018	1,297.50 -	1,297.50	30.00	10/2021 -	10/2021
127	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383]	9/2019	164.69 -	164.69	-	07/2021 -	07/2021
128	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]	5/2016	261.00 -	261.00	71.13	01/2021 -	01/2021
129	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309]	8/2017	1,342.00 -	1,342.00	6.30	08/2020 -	08/2020
130	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]	8/2017	255.40 -	255.40	6.53	08/2020 -	08/2020
131	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]	8/2019	1,255.00 -	1,255.00	106.50	10/2021 -	10/2021
	<u>Numaligarh Refinery Limited</u>						
132	NUMALIGARH REFINERY EXPANSION PROJECT - [N16000379]	1/2019	22,594.00 -	22,594.00	43.00	10/2024 -	10/2024
	<u>Oil & Natural Gas Corporation Limited</u>						
133	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]	4/2019	3,228.80 -	3,228.80	510.66	03/2022 -	03/2022
134	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	7/2016	249.85 250.00	265.49	152.67	05/2020 -	05/2020
135	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]	2/2019	2,292.46 -	2,292.46	815.60	05/2021 -	05/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
136	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]	5/2019	763.92 -	763.92	205.99	12/2020 -	12/2020
137	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	1,162.56	441.61	03/2026 -	03/2026
	<u>Oil India Limited</u>						
138	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN - [N16000356]	6/2016	224.75 -	224.75	98.98	08/2020 -	08/2020
139	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]	5/2016	406.00 -	406.00	106.50	10/2020 -	10/2020
	Total		1,11,714.84 -	1,13,007.98	22,474.40		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
140	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000273]	12/2018	587.44 -	587.44	250.00	09/2020 -	09/2020
141	PATRATU STPP-I (3X800MW) - [N18000275]	11/2017	18,668.00 -	18,668.00	2,409.34	03/2023 -	03/2023
142	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000274]	3/2019	349.00 -	349.00	125.00	11/2020 -	11/2020
	<u>Power Grid Corporation Of India Limited</u>						
143	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]	2/2017	5,070.13 -	5,070.13	3,270.48	04/2020 -	04/2020
144	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	3/2017	3,500.00 3,500.00	3,500.00	2,039.35	07/2020 -	07/2020
145	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]	11/2017	358.83 -	358.83	177.36	05/2020 -	05/2020
	<u>Satluj Jal Vidyut Nigam Limited</u>						
146	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]	3/2019	10,439.09 -	10,439.09	876.79	01/2024 -	01/2024
147	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	648.33	310.91	12/2021 -	12/2021
	<u>Thdc India Limited</u>						
148	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]	3/2019	11,089.42 -	11,089.42	909.73	09/2023 -	09/2023
149	AMELIA COAL MINE - [N18000252]	1/2017	2,104.21 -	1,587.16	309.90	09/2020 -	09/2020
	Total		52,814.45 -	52,297.40	10,678.86		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
150	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]	2/2015	2,449.91 -	2,449.91	218.30	03/2023 -	03/2023
151	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]	2/2016	9,968.00 -	9,968.00	-	03/2024 -	03/2024

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
152	PUNE-NASIK (265 KM) - [N22000354]	2/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024
153	DAUND - MANMAD (236 KM) - [N22000360]	2/2016	1,876.00 -	2,081.27	230.40	03/2023 -	03/2023
154	WARDHA-NANDED MAHARASHTRA - [N22000231]	4/2008	3,168.29 -	3,168.29	1,268.08	03/2023 -	03/2023
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
155	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	03/2020
	<u>East Central Railways</u>						
156	KOSI BRIDGE (NL), ECR - [220100304]	4/2002	499.41 -	516.02	404.10	03/2020 -	03/2020
	<u>North Central Railway</u>						
157	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	4/2015	668.70 668.00	680.00	330.00	03/2020 -	03/2020
158	JHANSI BINA DOUBLING - [N22000496]	9/2016	2,001.00 -	2,001.00	416.59	03/2021 -	03/2021
159	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]	3/2018	4,329.53 -	4,329.53	3.90	03/2023 -	03/2023
	<u>North East Frontier Railway</u>						
160	DIGARU-HOJAI (102 KM) - [N22000389]	4/2015	870.96 -	2,136.01	610.95	03/2021 -	03/2021
161	DIMAPUR-TIZIT NL - [N22000196]	4/2013	4,274.00 -	4,274.00	-	03/2020 -	03/2020
162	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	4/2010	242.22 -	471.00	69.09	03/2020 -	03/2020
163	NEW BG LINE FROM BYRNihat TO SHILLONG - [N22000205]	4/2010	906.46 -	6,000.60	263.12	03/2021 -	03/2021
164	MURKONGSELEK-PASIGHAT NL - [N22000208]	4/2011	414.84 -	661.00	123.00	03/2020 -	03/2020
	<u>North Eastern Railway</u>						
165	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	3/2007	243.78 -	895.00	106.55	12/2021 -	12/2021
166	HATHUA-BHATNI (N L) (NER) - [220100319]	4/2005	230.03 -	230.03	277.14	12/2022 -	12/2022
167	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]	4/2016	1,900.00 -	1,277.06	-	01/2022 -	01/2022
168	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]	4/2016	600.00 -	600.00	69.85	01/2022 -	01/2022
	<u>Northern Railway</u>						
169	CHANDIGARH-BADDI - [N22000467]	4/2007	328.14 -	1,540.00	234.79	03/2023 -	03/2023
	<u>National High Speed Rail Corporation Limited</u>						
170	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]	12/2015	1,08,000.00 -	1,08,000.00	6,708.69	12/2023 12/2023	12/2023
	<u>Rail India Technical And Economic Service</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
171	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498]	2/2016	393.98 -	393.98	290.45	03/2020 -	03/2020
172	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	392.54	03/2021 -	03/2021
	<u>Rail Vikas Nigam Ltd.</u>						
173	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	773.94 -	773.94	556.16	12/2024 -	12/2024
174	AHMEDABAD-BOTAD (GC) - [N22000140]	4/2012	975.62 -	1,082.32	1,202.24	12/2021 -	12/2021
175	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	1/1991	2,335.67 -	2,335.68	698.45	12/2024 -	12/2024
176	DHASA-JETALSAR (GC) - [N22000141]	4/2012	644.38 -	644.38	507.11	03/2021 -	03/2021
177	VIJAYAWADA-GUDUR - [N22000369]	4/2015	3,246.26 -	3,548.67	1,384.54	12/2023 -	12/2023
	<u>South Central Railway</u>						
178	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	4/2010	704.31 -	927.94	303.24	03/2020 03/2020	03/2020
	<u>South East Central Railway</u>						
179	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	9/2016	1,908.51 -	2,686.63	540.55	03/2023 03/2023	03/2023
	<u>South Western Railway</u>						
180	ARSIKERE-TUMKUR - [N22000332]	3/2015	578.00 -	578.00	565.04	03/2020 -	03/2020
181	YELAHANKA-PENJUKONDA - [N22000328]	5/2015	860.43 -	958.00	781.04	03/2020 -	03/2020
	<u>Southern Railway</u>						
182	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]	2/2015	1,700.00 -	1,003.00	252.02	03/2022 -	03/2022
	<u>Western Railway</u>						
183	CHOTTAUDEPUR-DHAR(NL) - [N22000138]	4/2007	1,347.26 -	1,347.26	756.98	03/2022 03/2022	03/2022
184	SURENDRA NAGAR RAJKOT - [N22000392]	4/2015	1,002.39 -	1,002.39	454.02	03/2021 03/2021	03/2021
	Total		1,79,095.40 -	2,25,639.97	42,503.93		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
185	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]	3/2018	293.10 -	293.10	63.14	08/2020 -	08/2020
186	NILAJPHATA TO BHANDARA - [N24001043]	1/2018	420.63 421.00	420.63	50.60	05/2020 -	05/2020
187	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]	10/2016	172.63 -	172.63	77.30	12/2020 -	12/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
188	BAMNI TO NAVAEGAON - [N24001110]	9/2017	241.69 242.00	241.69	109.29	04/2020 -	04/2020
189	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]	1/2018	283.15 -	283.15	42.22	05/2020 -	05/2020
190	ARDHAPUR TO HIMAYATNAGAR - [N24001079]	12/2017	426.06 426.00	426.06	91.97	06/2020 -	06/2020
191	MAHAD TO RAIGAD FORT - [N24001038]	7/2018	237.40 -	237.40	8.34	05/2020 -	05/2020
192	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]	2/2018	418.88 -	418.88	88.00	02/2020 -	02/2020
193	BHOGAN KHURD TO KASHEDI - [N24001132]	9/2017	743.21 743.00	743.21	131.87	06/2021 -	06/2021
194	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]	10/2016	171.90 -	171.90	23.19	08/2020 -	08/2020
195	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]	3/2018	293.64 -	293.64	134.32	08/2020 -	08/2020
196	REHABILITATION AND UPGRADATION OF ALLAHABAD - MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203]	10/2016	218.90 -	218.90	64.59	03/2020 -	03/2020
197	DHANGIPIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]	3/2018	217.14 217.00	217.14	100.77	02/2020 -	02/2020
198	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. - [N24001174]	10/2016	235.31 -	235.31	97.25	11/2020 -	11/2020
199	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]	3/2018	626.76 -	626.76	80.66	07/2020 -	07/2020
200	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]	5/2018	248.00 -	248.00	-	05/2020 -	05/2020
201	KALMATH TO ZARAP - [N24001137]	9/2016	1,338.13 1,338.00	1,338.13	959.51	03/2020 -	03/2020
202	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883]	3/2018	254.30 -	254.30	53.46	10/2020 -	10/2020
203	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA - [N24001139]	10/2016	218.94 219.00	218.94	120.69	03/2020 -	03/2020
204	PAHUR TO BODHWAD - [N24001084]	1/2017	244.93 -	244.93	75.23	05/2020 -	05/2020
205	SELDOH TO PANVAR - [N24001097]	7/2018	404.33 404.00	404.33	44.19	05/2020 -	05/2020
206	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]	10/2016	167.62 -	167.62	61.37	12/2020 -	12/2020
207	PATRADEVI TO KARASWADA 4L - [N24001004]	3/2017	634.32 -	634.32	109.33	05/2020 -	05/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
208	TALGAON TO KALMATH - [N24001136]	10/2016	904.70 905.00	904.70	604.05	03/2020 -	03/2020
209	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905]	3/2018	322.48 -	322.48	153.18	07/2020 -	07/2020
210	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208]	3/2018	288.30 -	288.30	41.74	08/2020 -	08/2020
211	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]	2/2018	426.52 -	426.52	225.51	04/2020 -	04/2020
212	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I - [N24001216]	12/2016	196.00 -	196.00	-	09/2021 -	09/2021
213	PANCHARAL TO MANDANGHAR - [N24001107]	7/2018	381.08 302.00	381.08	13.03	05/2020 -	05/2020
214	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131]	3/2018	212.99 -	212.99	99.21	06/2020 -	06/2020
215	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927]	3/2018	293.64 -	293.64	28.24	08/2020 -	08/2020
216	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148]	3/2016	599.34 -	599.34	492.15	01/2020 -	01/2020
217	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]	3/2018	263.89 -	242.05	139.94	04/2020 -	04/2020
218	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152]	9/2018	160.00 -	160.00	0.50	09/2021 -	09/2021
219	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]	3/2016	296.50 -	296.50	74.77	09/2020 -	09/2020
220	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 KM - [N24001230]	11/2018	281.45 -	281.45	2.36	12/2020 -	12/2020
221	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]	2/2018	206.13 -	206.13	127.86	06/2020 -	06/2020
222	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]	3/2018	185.18 -	185.18	79.93	02/2020 -	02/2020
223	KOTHARI TO DHANORA - [N24001073]	9/2018	301.38 301.00	301.38	59.42	08/2020 -	08/2020
224	WARDHA TO ARVI - [N24001150]	2/2018	313.58 -	313.58	32.96	04/2020 -	04/2020
225	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197]	3/2018	351.00 -	351.00	0.49	06/2021 -	06/2021
226	WADIGODRI TO DHANGRIPIMPRI - [N24001063]	3/2018	194.23 194.00	194.23	88.23	02/2020 -	02/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
227	JALKOT TO TOGRI - [N24001071]	7/2018	299.92 300.00	299.92	19.25	08/2020 -	08/2020
228	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]	1/2019	264.50 -	264.50	-	03/2021 -	03/2021
229	REHABILITATION AND UPGRADE OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]	3/2018	322.81 -	322.81	1.66	09/2020 -	09/2020
230	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH - - [N24001180]	3/2019	237.51 -	237.51	-	12/2022 -	12/2022
231	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]	3/2017	217.35 -	217.35	35.10	11/2020 -	11/2020
232	OSMANNAGAR TO KUNDRA - [N24001075]	9/2017	344.25 344.00	344.25	71.18	08/2020 -	08/2020
233	REHABILITATION AND UPGRADE TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906]	3/2018	173.24 -	173.24	56.66	06/2020 -	06/2020
	<u>National Highways Authority Of India</u>						
234	TWO-LANING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	3/2017	672.89 -	736.01	-	03/2020 -	03/2020
235	REHABILITATION AND UPGRADE OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]	3/2017	648.32 -	511.94	511.34	03/2020 -	03/2020
236	SIX-LANING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]	4/2017	894.00 -	929.32	760.00	04/2020 -	04/2020
237	FOUR LANNING OF VIKRAVANDI-SETHIAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]	3/2017	848.45 -	848.45	103.14	03/2020 -	03/2020
238	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]	8/2016	1,664.20 -	1,664.20	794.87	04/2020 -	04/2020
239	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]	3/2017	165.50 -	172.16	117.09	03/2020 -	03/2020
240	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]	3/2017	639.79 -	552.90	578.15	03/2020 -	03/2020
241	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	3/2017	744.64 -	982.00	-	03/2020 -	03/2020
242	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]	3/2017	239.68 -	235.90	91.24	03/2020 -	03/2020
243	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]	3/2017	296.19 -	254.00	254.85	03/2020 -	03/2020
	Total		23,362.60 -	23,413.98	8,245.39		
	<u>SHIPPING AND PORTS</u>						
	<u>Inland Waterways Authority Of India</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
244	JAL MARG VIKAS PROJECT - [N25000072]	1/2018	4,200.00 -	5,369.18	1,540.69	03/2023 03/2023	03/2023
	Total		4,200.00 -	5,369.18	1,540.69		
	<u>STEEL</u>						
	<u>Steel Authority Of India Limited (Sail)</u>						
245	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E - [N12000121]	12/2018	263.36 -	263.36	29.03	09/2020 -	09/2020
	Total		263.36 -	263.36	29.03		
	<u>URBAN DEVELOPMENT</u>						
	<u>Ahmedabad Metro Rail</u>						
246	SURAT METRO RAIL PROJECT - [N28000138]	3/2019	12,020.32 -	12,020.32	4.67	03/2024 -	03/2024
247	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137]	3/2019	5,384.17 -	5,384.17	4.35	03/2024 -	03/2024
	<u>Central Public Works Department</u>						
248	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]	11/2017	171.72 -	171.72	45.00	03/2020 11/2020	03/2020
249	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPUR NEW DELHI PHASE-I - [N28000128]	10/2016	1,180.00 -	1,100.80	9.96	07/2021 -	07/2021
250	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133]	2/2019	186.00 199.00	186.00	38.35	09/2020 -	09/2020
251	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]	10/2016	1,128.00 -	1,128.00	1.52	03/2022 -	03/2022
252	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]	12/2018	260.00 -	260.00	12.50	06/2021 -	06/2021
253	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]	11/2017	238.56 -	238.56	63.67	05/2020 -	05/2020
254	CONSTRUCTION OF GRAMEEN VIKAS BHAWAN (2BASEMENTS+ GROUND+9 FLOORS) FOR MINISTRY OF RURAL DEVELOPMENT - [N28000132]	11/2018	361.60 -	361.60	0.45	07/2021 -	07/2021
	<u>Delhi Metro Rail Corporation</u>						
255	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136]	5/2017	565.00 -	565.00	420.66	12/2020 -	12/2020
256	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS - [N28000135]	7/2019	24,948.65 -	24,948.65	78.44	03/2025 -	03/2025
	<u>Madhya Pradesh Metro Rail Co Limited</u>						
257	BHOPAL METRO RAIL - [N28000124]	11/2018	6,941.40 -	6,941.40	58.37	02/2023 -	02/2023
258	INDORE METRO RAIL - [N28000125]	11/2018	7,500.80 -	7,500.80	54.74	02/2023 -	02/2023
	<u>National Capital Region Transport Corp</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
259	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134]	3/2019	30,274.00 -	30,274.00	690.64	06/2025 -	06/2025
	Total		91,160.22 -	91,081.02	1,483.32		
	<u>WATER RESOURCES</u>						
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>						
260	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA - [N30000051]	8/2017	824.00 -	824.00	0.41	06/2022 -	06/2022
261	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]	5/2017	356.37 -	356.37	66.44	04/2021 -	04/2021
262	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026]	3/2018	230.06 -	230.06	-	07/2021 -	07/2021
263	I AND D AND STP AT CHAPPRA - [N30000028]	11/2018	236.15 -	236.15	0.06	12/2020 -	12/2020
264	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]	3/2017	277.42 -	277.42	85.87	05/2021 -	05/2021
265	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]	5/2017	191.62 -	191.62	37.70	11/2020 -	11/2020
266	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]	10/2017	254.13 -	254.13	0.05	09/2020 -	09/2020
267	SEWER NETWORKS, SPS AND STP, MUNGER - [N30000036]	3/2018	294.02 -	294.02	-	10/2021 -	10/2021
268	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]	3/2018	305.19 -	305.19	-	08/2021 -	08/2021
269	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]	12/2014	225.77 -	225.77	183.57	03/2020 -	03/2020
270	SAIDPUR SEWER NETWORK PATNA - [N30000039]	4/2015	268.63 -	268.63	192.80	01/2021 -	01/2021
271	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]	8/2017	578.89 -	578.89	0.29	06/2022 -	06/2022
272	SEWERAGE SCHEME AT PAHARI ZONE IVA S PATNA - [N30000041]	5/2017	184.86 -	184.86	103.13	05/2021 -	05/2021
273	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR - [N30000038]	4/2015	184.93 -	184.93	163.36	04/2020 -	04/2020
	<u>Delhi Jal Board</u>						
274	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014]	3/2017	665.78 -	665.78	94.40	12/2022 -	12/2022
275	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI - [N30000017]	12/2018	515.07 -	515.07	246.01	01/2021 -	01/2021
276	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]	5/2016	239.11 -	239.11	42.77	02/2022 -	02/2022
277	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015]	5/2016	211.79 -	211.79	39.14	12/2021 -	12/2021
278	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018]	5/2017	344.81 -	344.81	-	05/2020 -	05/2020
	<u>Kolkata Metropolitan Development Authority</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
279	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]	8/2017	185.22 -	185.22	-	12/2021 -	12/2021
280	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPUR - [N30000030]	3/2019	287.53 -	287.53	-	04/2022 -	04/2022
281	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA - [N30000034]	8/2017	307.12 -	307.12	-	09/2022 -	09/2022
282	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]	10/2017	164.93 -	164.93	-	12/2021 -	12/2021
283	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033]	3/2018	165.16 -	165.16	-	06/2022 -	06/2022
284	INTERCEPTION AND DIVERSION WITH STP AT HUGHLI-CHINSURAH - [N30000042]	5/2018	160.00 -	160.00	-	02/2022 -	02/2022
285	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048]	1/2018	172.10 -	172.10	-	12/2021 -	12/2021
286	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]	12/2014	272.32 -	272.32	191.36	04/2020 -	04/2020
287	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]	12/2018	234.31 -	234.31	-	04/2022 -	04/2022
288	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]	5/2018	198.43 -	198.43	-	02/2022 -	02/2022
289	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]	1/2019	384.96 -	384.96	-	04/2022 -	04/2022
<u>Uttar Pradesh Jal Nigam</u>							
290	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WORKS AT AGRA - [N30000023]	2/2019	317.19 -	317.19	-	08/2021 -	08/2021
291	MATHURA SEWERAGE SCHEME - [N30000019]	12/2017	460.45 -	460.45	56.83	12/2020 -	12/2020
292	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]	1/2019	231.79 -	231.79	-	12/2021 -	12/2021
293	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]	2/2019	681.78 -	681.78	-	06/2022 -	06/2022
294	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]	10/2017	213.62 -	213.62	-	03/2022 -	03/2022
295	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR - [N30000009]	10/2016	370.40 -	370.40	268.59	08/2020 -	08/2020
296	INTEGRATED PROJECT FOR DEVELOPMENT OF STPS IN ALLAHABAD ALONG WITH EXISTING ASSETS - [N30000007]	3/2018	904.00 -	904.00	-	09/2021 -	09/2021
297	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]	3/2019	298.12 -	298.12	-	07/2021 -	07/2021
298	REHABILITATION RENOVATION OF AGRA SEWERAGE SCHEME INTERCEPTION AND DIVERSION WORKS IN AGRA UTTAR PR - [N30000012]	12/2018	857.26 -	857.26	-	08/2021 -	08/2021
299	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010]	3/2018	967.23 -	967.23	-	09/2021 -	09/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
300	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022]	1/2019	206.05 -	206.05	1.57	10/2021 -	10/2021
301	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006]	5/2017	767.59 -	767.59	0.01	09/2021 -	09/2021
302	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH - [N30000013]	3/2019	271.39 -	271.39	-	08/2021 -	08/2021
	Total		15,467.55 -	15,467.55	1,774.36		
	Grand Total		5,65,214.72	6,14,270.42	1,11,962.58		

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Annexure - V

(January 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
	<u>Bhavini Limited</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,840.00	5,862.38	09/2010 -	10/2021	95.88
	<u>Nuclear Power Corporation Of India Limited</u>							
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	14,629.00	12/2015 -	09/2021	44.69
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]	10/2009	12,320.00 -	17,079.00	11,737.00	12/2016 -	03/2023	38.63
	Total		27,271.00 -	40,499.00	32,228.38			
	<u>CIVIL AVIATION</u>							
	<u>Airport Authority Of India Limited</u>							
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	314.61 -	441.33	85.79	09/2018 -	06/2020	40.28
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI [N04000083]	12/2016	859.86 -	860.00	232.44	03/2021 -	03/2021	.02
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]	09/2015	338.93 -	339.00	213.50	06/2019 -	-	.02
	Total		1,513.40 -	1,640.33	531.73			
	<u>COAL</u>							
	<u>Eastern Coal Fields Limited</u>							
7	RANIGANJ MASTER PLAN - [N06000163]	08/2009	2,661.73 -	5,146.48	364.72	08/2019 -	08/2024	93.35
	<u>Neyveli Lignite Corporation</u>							
8	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	06/2011	5,907.11 -	7,080.41	6,954.15	12/2015 -	03/2020	19.86
9	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80	8,596.47	11/2021 -	11/2021	.00
	<u>Singareni Colliers Company Limited</u>							
10	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	416.88	03/2012 -	03/2023	16.86
11	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	326.69	03/2012 -	03/2024	80.24

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
12	KAKATIYAKHANI OPENCASE-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	99.56	03/2019 -	03/2020	11.42
13	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 -	473.22	18.60	03/2015 -	03/2021	5.85
14	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	12.27	03/2015 -	03/2021	114.60
	<u>South-Eastern Coal Fields Limited</u>							
15	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	195.34	03/2015 -	03/2020	201.44
	<u>Western Coal Fields Limited</u>							
16	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	313.34	118.18	03/2021 -	03/2024	12.85
17	BHANEAGAN OC - [N06000121]	02/2015	187.94 -	409.68	129.61	03/2023 -	03/2023	117.98
18	ADASA UG TO OC - [N06000133]	08/2015	288.90 -	333.43	38.82	03/2023 -	03/2024	15.41
	Total		28,387.67 -	33,184.03	17,271.29			
	<u>COMMERCE AND INDUSTRY</u>							
	<u>India International Convention And Expo Centre</u>							
19	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]	11/2017	4,773.00 -	5,178.00	1,309.65	12/2019 -	09/2020	8.49
	Total		4,773.00 -	5,178.00	1,309.65			
	<u>HEALTH AND FAMILY WELFARE</u>							
	<u>Central Public Works Department</u>							
20	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]	03/2019	1,577.00 -	1,828.00	-	09/2025 -	09/2025	15.92
	<u>Hospital Services Consultancy Corporation Ltd</u>							
21	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	02/2013	414.11 -	499.23	337.32	11/2013 -	09/2020	20.55
22	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 -	270.00	210.75	05/2017 -	06/2020	32.07
23	AIIMS - OPD(NEW) - [N21000009]	08/2014	293.65 -	325.00	304.62	05/2017 -	01/2020	10.68
24	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]	12/2014	168.90 -	191.20	169.51	05/2017 -	07/2019	13.20
25	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	09/2014	505.58 -	585.00	586.96	03/2018 -	09/2019	15.71
26	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]	07/2016	152.95 -	177.92	147.31	02/2018 -	03/2020	16.33

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
27	CNCI KOLKATA WEST BENGAL - [N21000015]	08/2016	244.00 -	248.00	224.92	09/2018 -	05/2019	1.64
28	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	08/2017	272.19 -	272.54	204.08	03/2019 -	03/2020	.13
29	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]	12/2017	156.56 -	156.64	80.28	-	05/2020	.05
30	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]	01/2018	249.01 -	249.07	149.26	-	05/2020	.02
	<u>National Building Construcion Corporation Ltd</u>							
31	AIIMS BILASPUR - [N21000028]	04/2018	1,351.00 -	1,471.00	421.44	09/2021 -	09/2021	8.88
	Total		5,589.39 -	6,273.60	2,836.45			
	<u>HUMAN RESOURCE DEVELOPMENT</u>							
	<u>Rail India Technical And Economic Service</u>							
32	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]	09/2013	484.32 -	626.26	-	09/2014 -	12/2020	29.31
	Total		484.32 -	626.26	.00			
	<u>PETROLEUM</u>							
	<u>Bharat Petroleum Corporation Limited</u>							
33	HALDIA LPG IMPORT FACILITY - [N16000223]	03/2015	694.00 -	1,097.54	856.34	10/2018 -	02/2020	58.15
34	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29 -	5,245.96	4,137.20	08/2018 -	02/2020	14.33
35	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]	12/2015	1,112.00 -	1,507.24	566.00	06/2019 -	02/2022	35.54
	<u>Gas Authority Of India Limited</u>							
36	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	02/2015	749.00 -	842.00	606.89	02/2020 -	02/2020	12.42
37	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]	06/2009	2,915.00 2,915.00	4,915.00	2,784.58	12/2012 -	02/2022	68.61
	<u>Hindustan Petroleum Corporation Limited</u>							
38	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	07/2016	20,928.00 -	26,264.00	8,584.07	07/2020 -	07/2022	25.50
39	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]	09/2015	4,199.00 -	5,060.00	3,446.40	03/2020 -	03/2020	20.50
	<u>Indian Oil Corporation Limited</u>							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
40	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	356.62	10/2017 -	-	17.66
41	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	01/2015	1,823.00 -	3,027.90	1,030.43	12/2020 -	12/2020	66.09
42	PARADIP HYDERABAD PIPELINE - [N16000194]	01/2015	2,321.00 -	3,338.00	2,123.21	12/2020 -	08/2020	43.82
43	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]	05/2016	664.00 -	729.40	664.73	12/2020 -	02/2020	9.85
44	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	05/2016	4,497.00 -	6,025.00	1,588.02	12/2018 -	02/2021	33.98
	<u>Indian Strategic Petroleum Reserves Ltd</u>							
45	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	1,549.85	01/2012 -	-	70.49
	<u>Mangalore Refinery And Petrochemicals Limited</u>							
46	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]	10/2015	135.00 171.00	170.70	156.65	03/2019 -	-	26.44
47	SEA WATER DESALINATION PLANT - [N16000319]	11/2017	581.00 -	621.00	154.66	03/2020 -	11/2020	6.88
	<u>Oil & Natural Gas Corporation Limited</u>							
48	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79 -	1,683.06	1,386.15	05/2013 -	02/2020	95.30
49	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	1,933.09	03/2015 -	03/2020	29.42
50	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	2,369.08	04/2018 -	05/2020	1.77
51	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	823.27 -	910.23	441.81	03/2023 -	03/2022	10.56
52	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	07/2016	249.85 250.00	265.49	152.67	05/2020 -	05/2020	6.26
53	DEVELOPMENT OF B-147 FIELD - [N16000292]	02/2017	546.15 -	565.15	468.71	11/2019 -	03/2020	3.48
54	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]	02/2017	4,006.83 -	4,475.92	2,975.26	05/2021 -	12/2021	11.71
55	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]	02/2019	3,660.71 -	3,740.05	373.79	04/2021 -	05/2021	2.17
	<u>Oil India Limited</u>							
56	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	438.84	268.45	03/2017 -	06/2020	24.47

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
57	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	565.63	03/2015 -	-	37.72
58	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	01/2018	543.91 -	682.90	71.46	02/2020 -	06/2020	25.55
	Total		63,973.09 -	81,125.47	39,611.75			
	<u>POWER</u>							
	<u>National Hydro-Electric Power Corporation</u>							
59	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	9,997.11	7,761.19	09/2009 -	12/2021	155.06
60	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	19,496.34	11,842.12	09/2010 -	08/2023	210.19
	<u>National Thermal Power Corporation</u>							
61	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	12,865.92	12,503.29	01/2018 -	03/2020	10.55
62	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	5,867.38	4,346.71	03/2013 -	12/2021	96.99
63	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	09/2014	9,188.98 -	10,016.10	7,036.74	07/2019 -	09/2020	9.00
64	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 -	13,740.53	10,182.96	12/2018 -	08/2020	9.64
65	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,164.05	9,965.78	06/2019 -	03/2022	5.55
66	RAMMAM-III HEPP (3X40 MW) - [N18000178]	09/2014	1,381.84 -	1,592.34	526.08	09/2019 -	11/2022	15.23
67	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	9,583.00	8,056.25	07/2012 -	09/2020	79.02
68	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	17,304.00	14,367.00	05/2018 -	06/2021	33.47
69	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]	04/2012	9,750.89 -	12,176.28	10,103.00	02/2017 -	06/2020	24.87
70	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	21,312.11	16,928.07	10/2011 -	08/2021	145.16
71	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	12,826.56	10/2017 -	03/2020	7.55
72	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	07/2012	1,527.00 -	1,801.07	148.93	08/2017 -	-	17.95
73	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	03/2015	9,870.51 -	11,148.86	9,430.15	01/2020 -	02/2020	12.95
74	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	3,365.00	10/2017 -	-	7.41
	<u>North East Electric Power Corporation</u>							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
75	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [N180100239]	12/2004	2,496.90 -	7,927.34	7,743.76	12/2009 06/2016	06/2020	217.49
	<u>Power Grid Corporation Of India Limited</u>							
76	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]	10/2008	4,824.12 -	5,071.94	4,595.36	10/2012 -	03/2020	5.14
77	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	14,719.10	12,824.45	08/2013 -	03/2022	32.24
78	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	1,283.60	04/2016 -	02/2020	38.61
79	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	546.36	470.71	11/2016 -	03/2020	4.61
80	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03	200.16	07/2017 -	01/2020	27.92
81	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	590.30	06/2014 -	02/2020	31.17
82	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,072.36	1,402.48	12/2018 -	12/2020	90.82
83	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,880.36	1,886.30	12/2018 -	12/2020	34.61
	<u>Thdc India Limited</u>							
84	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	4,397.80	1,858.35	06/2013 -	12/2022	76.51
	Total		1,59,920.84 -	2,30,763.07	172,245.30			
	<u>RAILWAYS</u>							
	<u>Central Railways</u>							
85	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89 -	1,377.48	318.59	03/2021 -	03/2022	73.73
86	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 -	312.00	293.06	03/2019 -	03/2020	69.51
87	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 -	4,517.49	2,495.07	03/2021 -	03/2022	98.88
88	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024	120.28
89	VAIBHAVWADI-KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 -	3,438.51	-	03/2024 -	-	25.04
90	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	230.40	03/2023 -	03/2023	10.94
	<u>Container Corporation Of India</u>							
91	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 -	235.00	10.88	03/2019 -	12/2020	.21
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
92	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]	10/2006	11,589.00 30,357.00	28,181.00	-	-	-	143.17
93	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020	03/2020	207.99
	<u>East Central Railways</u>							
94	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	03/1999	1,033.07 -	3,376.00	3,349.65	-	03/2021	226.79
95	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	04/2003	528.65 -	2,066.78	1,454.19	-	03/2023	290.95
96	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	477.88 283.95	751.55	674.58	03/2012	03/2020	57.27
97	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	324.73 -	1,050.00	1,041.96	03/2012	03/2020	223.35
98	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	614.45	311.33	-	03/2022	277.26
99	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	499.41 -	516.02	404.10	03/2020	03/2020	3.33
100	SAMASTIPUR-DARBANGHA - [N22000329]	05/2015	380.00 -	519.33	195.83	-	02/2023	36.67
101	KODERMA-TILAIYA (NL), ECR - [220100305]	04/2002	459.91 -	1,625.87	544.36	-	03/2021	253.52
102	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 -	549.75	15.55	-	-	32.26
103	BIHTA-AURANGABAD (NL) - [N22000170]	04/2008	326.20 -	2,995.01	1.94	-	03/2024	818.15
104	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	325.00 -	735.20	367.62	-	03/2021	126.22
105	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	378.56 -	1,858.75	377.77	-	03/2022	391.01
106	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	1,006.00	24.16	-	-	376.78
107	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]	04/2004	372.14 -	1,470.50	849.10	-	03/2021	295.15
108	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]	04/2009	548.00 -	819.01	525.18	03/2020	03/2022	49.45
109	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	440.00	432.20	-	01/2020	106.56
110	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	546.71	541.43	07/2014	-	64.60
111	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 -	1,215.54	156.95	03/2021	03/2022	63.37
112	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 -	1,185.73	60.65	03/2021	03/2022	62.06
113	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]	04/1998	180.82 -	726.31	521.48	-	10/2019	301.68

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
114	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476	04/1991	329.39 -	1,483.14	1,060.33	- -	12/2021	350.27
	<u>East Coast Railway</u>							
115	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	810.78 -	1,928.07	780.24	06/2021 -	06/2024	137.80
116	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	2,923.13 -	3,791.66	1,270.24	03/2009 -	06/2024	29.71
117	SAMBALPUR-TALCHER DOUBLING - [N22000315	03/2011	1,111.99 -	1,539.28	972.93	02/2019 -	03/2022	38.43
118	KIRANDUL - JAGDALPUR DOUBLING - [N22000318	12/2012	1,160.00 -	1,160.83	749.76	03/2020 -	03/2023	.07
119	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319	03/2012	155.81 -	238.03	205.65	03/2020 -	03/2021	52.77
120	KOTTAVALSA - KORAPUT DOUBLING - [N22000377	04/2015	2,499.71 -	3,382.95	447.56	03/2022 -	03/2024	35.33
121	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380	04/2015	701.61 -	810.02	139.27	11/2018 -	03/2022	15.45
	<u>Eastern Railways</u>							
122	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	1,188.91 -	1,619.48	872.43	03/2019 12/2009	03/2025	36.22
123	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	607.09 -	1,425.44	637.56	02/2013 -	03/2024	134.80
124	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235	04/2010	365.17 -	527.54	1.76	- -	03/2025	44.46
125	HANSDIHA-GODDA NL - [N22000236	04/2011	542.18 -	693.80	474.79	03/2020 -	03/2021	27.96
126	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238	04/2011	175.80 -	260.83	260.83	- -	03/2021	48.37
127	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	12.02
128	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240	04/2010	494.54 -	494.59	32.00	03/2005 -	03/2025	.01
129	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241	04/2000	297.47 -	298.22	52.09	- -	03/2025	.25
130	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243	04/2009	499.96 -	680.68	159.70	02/2012 -	03/2025	36.15
131	MONIGRAM- NIMTITA - [N22000301	04/2012	250.93 -	310.70	287.10	- -	03/2024	23.82
132	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302	04/2012	255.64 -	272.20	196.05	- -	09/2021	6.48

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
133	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216	04/1987	406.99 -	545.70	148.49	03/2006 -	03/2025	34.08
134	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217	04/2007	450.00 -	1,261.34	-	- -	03/2025	180.30
135	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218	04/2010	172.03 -	260.10	10.73	- -	03/2025	51.19
136	PIRPAINTI-JASIDIH - [N22000219	04/2013	915.98 -	2,137.81	300.18	03/2022 -	03/2025	133.39
137	BANDEL-BOINCHI 3RD LINE - [N22000221	04/2011	288.35 -	402.48	402.48	- -	03/2020	39.58
138	PIRPAINTI-BHAGALPUR - [N22000222	04/2011	261.38 -	492.84	492.84	- -	05/2019	88.55
139	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224	04/2001	923.52 -	995.10	507.56	03/2016 -	03/2025	7.75
140	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225	04/2005	595.51 -	769.40	103.08	03/2017 -	03/2025	29.20
<u>Indian Railway Construction Company Limited</u>								
141	GEVRA ROAD PENDRA ROAD - [N22000488	02/2014	2,288.00 -	4,970.11	635.13	03/2022 -	12/2022	117.23
<u>Metropolitan Rapid Transport Projects</u>								
142	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69 -	3,404.92	3,837.57	12/2006 -	-	224.37
143	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	2,980.41	1,457.78	03/2004 -	03/2021	501.57
144	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028	04/2006	495.74 -	734.01	445.91	06/2013 -	-	48.06
145	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	75.91
<u>North Central Railway</u>								
146	ETAWAH-MAINPURI (NL),NCR - [220100318	04/1997	120.00 -	346.00	345.51	12/2008 -	-	188.33
147	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	04/2011	2,912.96 -	3,845.60	148.26	03/2022 -	12/2024	32.02
148	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372	04/2015	668.70 668.00	680.00	330.00	03/2020 -	03/2020	1.69
<u>North East Frontier Railway</u>								
149	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135	04/1983	297.32 -	614.00	275.07	03/2019 -	03/2020	106.51
150	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	2,393.47 -	5,021.45	3,183.01	03/2014 -	03/2022	109.80

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
151	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [N220100266	04/2000	1,180.19 -	4,541.00	3,346.08	12/2008 -	03/2021	284.77
152	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [N220100288	04/2003	4,454.17 -	12,524.00	9,599.02	03/2011 -	03/2022	181.17
153	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N220000086	09/2006	385.20 -	1,532.00	652.15	03/2019 -	03/2020	297.72
154	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N220000087	09/2006	532.87 -	2,145.00	935.62	03/2019 -	03/2020	302.54
155	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124	04/2006	2,326.52 -	5,806.81	876.09	03/2015 -	10/2021	149.59
156	KISHANGANJ JALALGARH, NL, NEFR - [N22000101	04/2008	333.76 -	360.00	6.74	- -	03/2022	7.86
157	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	4,084.69	332.23	12/2015 -	-	204.95
158	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183	04/2013	1,798.00 -	2,496.67	0.04	03/2019 -	-	38.86
159	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193	04/2010	221.42 -	380.00	38.18	- -	03/2022	71.62
160	AGARTALA-AKHAURA NL - [N22000195	04/2012	569.63 -	670.00	82.81	03/2020 -	09/2021	17.62
161	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205	04/2010	906.46 -	6,000.60	263.12	03/2021 -	03/2021	561.98
162	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206	04/2010	242.22 -	471.00	69.09	03/2020 -	03/2020	94.45
163	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207	04/2010	241.52 -	373.87	273.20	- -	06/2021	54.80
164	MURKONGSELEK-PASIGHAT NL - [N22000208	04/2011	414.84 -	661.00	123.00	03/2020 -	03/2020	59.34
165	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209	04/1999	819.23 -	1,871.00	1,082.01	- -	-	128.39
166	AMBAR FALAKATA TO NEW MAYNAGURI - [N22000210	04/2011	314.00 -	728.00	731.27	03/2019 -	03/2020	131.85
167	DIGARU-HOJAI (102 KM) - [N22000389	04/2015	870.96 -	2,136.01	610.95	03/2021 -	03/2021	145.25
168	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390	04/2016	602.27 -	612.00	344.08	12/2021 -	03/2020	1.62
169	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHOWA-JAIN - [N22000499	02/1999	380.60 -	1,871.00	1,087.60	04/2010 -	-	391.59
<u>North Eastern Railway</u>								
170	KICHHA-KHATIMA (NL) - NER - [N220100317	04/2003	142.45 -	228.40	0.15	- -	-	60.34

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
171	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	-	- -	-	8.10
172	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 -	1,409.09	-	- -	-	358.99
173	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 -	895.00	106.55	12/2021 -	12/2021	267.13
174	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	370.93	01/2019 -	01/2020	61.80
175	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 -	644.00	-	- -	-	.16
176	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	9.63	04/2016 -	06/2020	.16
177	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]	04/2017	1,343.00 -	1,476.15	-	01/2018 -	-	9.91
178	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]	04/2016	602.50 -	714.34	34.88	- -	-	18.56
	<u>North Western Railway</u>							
179	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	886.41	568.73	02/2019 -	06/2021	116.16
180	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	685.99	99.38	03/2020 -	04/2022	14.33
181	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]	05/2015	873.71 -	1,980.21	4.60	- -	-	126.64
182	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	348.55	248.71	12/2019 -	02/2021	41.64
183	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	4,262.36	185.90	- -	-	104.65
184	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	350.45	232.02	10/2018 -	12/2019	47.91
185	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]	04/2013	822.00 -	1,099.54	-	- -	-	33.76
186	PUSHKAR-MERTA - [N22000151]	04/2013	323.00 -	432.22	-	- -	-	33.81
187	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	303.56	285.01	11/2019 -	12/2020	42.26
188	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	410.00	381.92	02/2019 -	02/2020	69.36
	<u>Northern Railway</u>							
189	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	197.17	106.97	- -	03/2024	25.87
190	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	750.00	290.62	12/2011 -	03/2021	161.32
191	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]	04/2007	336.91 -	791.39	517.05	- -	03/2022	134.90

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
192	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63	233.23	- -	06/2020	57.68
193	UNCHAHAAR-AMETHI - [N22000294]	04/2012	1,229.00 -	1,230.00	103.72	- -	03/2023	.08
194	QADIAN-BEAS - [N22000295]	04/2011	205.22 -	841.90	1.73	- -	03/2024	310.24
195	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,200.00	668.77	07/2012 -	03/2024	388.89
196	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	27,949.00	20,501.11	11/2002 -	06/2022	1,017.96
197	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 -	1,540.00	234.79	03/2023 -	03/2023	369.31
198	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 -	859.00	835.35	03/2016 -	03/2021	37.44
	<u>Rail Vikas Nigam Ltd.</u>							
199	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	1,185.64 -	1,844.47	1,883.44	12/2017 -	03/2020	55.57
200	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	396.00	388.21	03/2009 03/2009	06/2020	196.83
201	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	04/2010	2,913.51 -	4,639.00	871.04	03/2016 -	03/2025	59.22
202	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	2,966.99 -	7,000.00	472.83	12/2026 -	12/2025	135.93
203	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 -	2,900.00	1,815.11	03/2023 -	03/2024	36.34
204	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,724.30	2,307.00	03/2016 -	03/2025	19.54
205	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	40.13	03/2014 -	12/2025	18.95
206	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]	03/2012	1,503.71 -	2,200.00	1,966.03	03/2020 -	03/2022	46.30
207	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	975.62 -	1,082.32	1,202.24	12/2021 -	12/2021	10.94
208	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	720.70	03/2016 -	12/2020	29.06
209	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.67	1,384.54	12/2023 -	12/2023	9.32
210	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,200.00	1,209.55	03/2019 -	03/2020	29.45
211	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 -	2,300.00	2,131.56	03/2020 -	03/2021	222.36
212	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 -	2,335.68	698.45	12/2024 -	12/2024	.00

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
213	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 -	1,500.00	1,451.81	03/2020 -	03/2021	58.22
214	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 -	1,120.00	1,046.08	03/2019 -	06/2022	18.78
	<u>Railway Electrification</u>							
215	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	141.55	03/2012 -	-	60.77
	<u>South Central Railway</u>							
216	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 -	2,120.16	561.18	03/2009 -	03/2023	102.85
217	MANUGURU-RAMAGUNDAM - [N22000259]	04/2013	1,112.00 -	2,911.84	0.92	- -	-	161.86
218	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	04/2012	1,856.95 -	1,952.68	329.00	03/2023 -	03/2024	5.16
219	BHADRACHALAM-KOVVUR - [N22000264]	04/2012	923.23 -	2,184.83	2.46	- -	-	136.65
220	NADIKUDE-SRI KALAHASTI - [N22000286]	04/2011	2,288.70 -	2,643.25	860.07	03/2021 -	03/2024	15.49
221	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	704.31 -	927.94	303.24	03/2020 -	03/2020	31.75
222	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	164.36 -	1,050.00	999.64	02/2009 -	-	538.84
223	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	1,723.00 1.00	3,472.59	970.69	03/2000 -	03/2021	101.54
224	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	458.25 -	458.26	3.83	- -	-	.00
225	MANMAD-PARBHANI-NANDED-SECUNDERABAD- GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	04/2017	119.73 185.00	449.39	298.13	03/2022 -	12/2022	275.34
	<u>South East Central Railway</u>							
226	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	1,413.76	1,351.73	- -	01/2020	268.37
227	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	511.86 -	1,756.00	1,679.29	04/2020 -	01/2021	243.06
228	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,908.51 -	2,686.63	540.55	03/2023 -	03/2023	40.77
229	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438]	04/2010	585.93 -	1,268.32	687.95	02/2019 -	12/2020	116.46
230	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00 -	852.50	39.69	12/2021 -	03/2023	272.27
231	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]	04/2008	872.00 -	1,226.51	1,066.54	12/2019 -	03/2020	40.65
232	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	04/2015	1,973.00 -	1,973.64	185.98	03/2021 -	03/2023	.03

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
233	ANUPPUR-KATNI - [N22000485]	04/2015	1,370.00 -	1,370.94	332.76	12/2021 -	03/2023	.07
	<u>South Eastern Railway</u>							
234	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00	182.49	03/2007 03/2007	-	160.76
235	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	377.00	183.96	12/2016 -	03/2020	153.41
236	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	620.00	40.99	- -	03/2025	131.89
237	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	651.00 -	1,009.00	7.96	03/2015 -	03/2025	54.99
238	CHAMPAPJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	54.46	03/2015 -	-	53.44
239	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	358.68	278.34	12/2018 -	08/2020	38.92
240	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	1,312.96	610.19	03/2020 -	03/2021	35.38
241	BONDAMUNDA RANCHI DOUBLING - [N22000396]	03/2016	1,724.20 -	1,993.24	469.79	03/2021 -	12/2021	15.60
242	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 -	2,373.00	485.04	03/2003 -	03/2030	130.97
	<u>South Western Railway</u>							
243	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	-	- -	12/2023	24.09
244	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	-	- -	12/2023	57.65
245	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	0.34	- -	12/2023	14.14
246	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	-	- -	12/2023	12.38
247	YELAHANKA-PENUKONDA - [N22000328]	05/2015	860.43 -	958.00	781.04	03/2020 -	03/2020	11.34
248	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 -	1,870.41	1,056.97	03/2019 -	03/2021	15.84
249	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78 -	890.00	461.80	03/2017 -	03/2020	38.03
	<u>Southern Railway</u>							
250	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' AGASTIYAMPALLI [N22000079]	09/2007	724.69 -	2,072.50	1,471.60	02/2019 -	02/2020	185.98
251	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	227.40 -	900.00	63.28	- -	-	295.78
252	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	582.83 -	2,300.00	243.44	- -	-	294.63
253	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	303.98 -	980.00	683.11	03/2020 -	03/2021	222.39

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
254	ANGAMALI-SABARIMALA (N.L.)(SR) - [N220100252]	10/1998	1,566.00 -	2,815.62	264.28	- -	-	79.80
255	ATTIPPATTU PUTTUR - [N22000184]	04/2008	151.84 -	1,105.00	3.34	02/2019 -	-	627.74
256	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	2,300.00	2.28	- -	-	339.33
257	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	0.62	- -	-	78.78
258	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	305.22	- -	-	180.17
259	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	457.08	373.51	- -	-	69.20
260	ERODE-PALANI - [N22000199]	04/2008	288.57 -	1,140.00	1.63	- -	-	295.05
261	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	197.11	- -	03/2020	173.71
262	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	931.98 -	951.24	753.41	- -	03/2020	2.07
263	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215]	04/2011	120.70 -	1,800.00	187.92	03/2019 -	12/2019	1,391.30
264	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]	10/2013	187.26 -	231.67	167.12	04/2014 -	03/2020	23.72
265	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	02/1996	268.87 -	950.00	927.86	03/2005 -	-	253.33
266	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00 -	1,182.31	446.00	03/2020 -	06/2021	55.57
<u>West Central Railway</u>								
267	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60 -	2,909.99	1,975.34	03/2021 -	03/2023	585.35
268	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	8,248.50	1,986.78	05/2008 -	03/2023	3,230.57
269	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13 -	1,247.64	228.36	03/2022 -	09/2022	114.32
<u>Western Railway</u>								
270	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	3,503.69 -	3,975.22	1,801.98	03/2022 -	03/2023	13.46
271	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]	04/2006	117.36 196.95	202.35	809.40	03/2011 -	-	72.42
272	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	125.76	03/2012 -	03/2022	1.06
273	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	04/2008	829.74 -	1,310.23	1,532.69	03/2020 -	03/2021	57.91

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
274	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	858.96	534.00	03/2019 -	03/2022	167.87
275	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]	02/1991	551.51 -	809.07	635.52	03/2019 -	03/2020	46.70
	Total		1,87,179.52 -	4,10,551.11	161,554.64			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>							
276	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]	12/2011	156.26 227.00	247.95	175.00	- -	-	58.68
277	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]	11/2010	624.41 -	992.67	886.01	03/2011 -	12/2020	58.98
278	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]	12/2011	156.63 276.00	276.00	147.65	02/2012 -	-	76.21
279	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]	08/2010	193.69 -	327.92	258.71	10/2010 -	06/2021	69.30
280	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]	03/2012	207.03 -	389.45	308.09	05/2012 -	12/2019	88.11
281	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]	01/2013	182.28 -	269.14	185.49	02/2013 -	12/2019	47.65
282	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]	03/2015	258.97 -	268.92	-	08/2015 -	-	3.84
283	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]	03/2015	157.18 162.00	162.00	-	07/2015 -	-	3.07
284	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]	03/2015	280.16 -	290.59	219.47	- -	-	3.72
285	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	01/2014	255.75 348.00	348.43	290.12	09/2017 -	-	36.24
286	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]	10/2013	445.89 -	653.29	464.05	03/2017 -	-	46.51
287	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]	11/2013	497.05 -	881.05	624.54	05/2017 -	05/2020	77.26

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
288	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391	11/2015	889.24 -	904.82	739.41	- -	-	1.75
289	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396	11/2010	470.20 -	630.36	386.98	02/2011 -	-	34.06
290	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398	01/1991	282.41 -	322.01	278.45	08/2016 -	-	14.02
291	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401	11/2011	954.43 -	1,191.51	235.61	09/2015 -	10/2021	24.84
292	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402	01/1991	358.22 -	377.64	325.19	10/2016 -	-	5.42
293	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407	10/2015	333.21 -	353.89	256.11	11/2015 -	-	6.21
294	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411	11/2014	218.31 -	307.47	263.85	02/2018 -	-	40.84
295	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415	08/2010	195.04 -	377.99	312.41	10/2010 -	-	93.80
296	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531	01/1991	319.68 -	369.77	113.67	- -	-	15.67
297	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639	03/2014	191.50 192.00	192.00	136.19	05/2016 -	-	.26
298	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645	08/2013	171.96 172.00	172.00	88.30	06/2016 -	-	.02
299	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782	03/2018	460.73 -	461.00	-	- -	-	.06
300	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820	11/2017	237.80 -	238.00	7.48	11/2019 -	-	.08
301	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O - [N24000871	08/2014	600.87 720.97	720.97	659.24	11/2017 -	05/2019	19.99
302	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873	08/2014	823.20 937.76	937.76	751.29	11/2017 -	06/2019	13.92
303	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874	03/2016	271.17 291.20	291.20	110.98	11/2018 -	11/2019	7.39
304	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885	03/2016	160.27 -	213.97	20.11	08/2019 -	08/2021	33.51

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
305	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887	06/2016	236.78 -	263.26	59.92	08/2019 -	08/2021	11.18
306	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889	04/2014	279.70 398.22	398.52	322.91	08/2017 -	07/2019	42.48
307	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890	03/2018	217.22 -	226.88	86.83	08/2018 -	06/2020	4.45
308	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928	10/2015	333.21 -	355.89	294.81	12/2015 -	01/2020	6.81
309	NAGAU-BIKANER OF NH-11 (2L+PS) UNDER PPP. - [N24000954	01/2012	378.07 -	478.73	188.98	01/2014 -	-	26.62
310	DEVELOPMENT AND OPERATION OF BIKANER-SURATGARH SECTION OF NH-15 BY 2L+PS IN THE STATE OF RAJASTHAN - [N24000956	03/2009	501.00 -	671.54	659.98	09/2013 -	-	34.04
311	BHOKAR TO SARSAM - [N24001128	02/2017	295.09 -	295.99	179.64	07/2019 -	-	.31
312	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144	10/2013	445.89 653.00	653.29	469.64	03/2017 -	10/2019	46.51
313	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151	11/2017	392.33 -	428.55	253.99	03/2018 -	09/2020	9.23
314	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181	08/2010	186.96 -	305.61	279.13	09/2014 -	06/2020	63.46
315	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219	01/2016	476.20 544.00	544.00	372.74	09/2016 -	-	14.24
316	WIDENING OF SL TO 2 L KM. 107-184.80 SUKUMA TO KONTA ON NH 221 - [N24001223	03/2010	179.89 271.00	271.00	-	03/2013 -	-	50.65
317	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1 - [N24001225	12/2010	169.26 299.00	299.00	-	01/2019 -	-	76.65
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>							
318	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676	12/2016	138.93 155.00	155.00	79.91	01/2017 -	01/2020	11.57
319	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686	03/2016	373.07 -	387.00	216.07	08/2016 -	03/2020	3.73
320	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695	04/2017	388.00 -	447.37	155.85	10/2017 -	-	15.30
	<u>National Highways Authority Of India</u>							
321	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 -	520.00	492.41	02/2009 -	07/2019	85.71

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
322	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	340.14	319.96	04/2009 -	08/2019	70.23
323	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279	12/2003	167.64 -	435.78	427.96	11/2008 -	01/2014	159.95
324	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	255.23	251.39	11/2008 -	08/2013	64.62
325	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049	12/2003	160.00 -	167.98	223.81	05/2008 -	06/2019	4.99
326	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	655.17	655.17	07/2009 -	10/2018	234.27
327	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,967.50	3,990.72	11/2011 -	03/2020	167.82
328	INDORE-DEWAS(NH-3) - [N24000159	11/2010	325.00 -	475.00	469.54	05/2013 -	-	46.15
329	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063	12/2003	217.61 -	360.84	454.21	04/2010 -	07/2019	65.82
330	NALBARI T BIJNI (AS-7) - [N24000048	12/2003	208.00 -	230.00	340.21	04/2008 -	03/2020	10.58
331	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233	04/2014	1,266.60 -	1,544.00	1,446.45	09/2016 -	-	21.90
332	NASHRI- CHANANI - [N24000162	05/2011	2,159.00 -	2,519.00	4,707.04	06/2015 -	-	16.67
333	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188	05/2011	511.54 -	591.00	571.86	11/2013 -	03/2020	15.53
334	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224	10/2012	1,928.22 -	2,945.00	2,467.00	04/2015 -	06/2020	52.73
335	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347	08/2015	723.54 -	1,286.84	1,163.65	02/2018 -	-	77.85
336	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435	10/2015	531.13 -	727.00	524.15	05/2018 -	09/2020	36.88
337	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441	10/2015	593.26 -	636.24	490.35	05/2018 -	06/2020	7.24
338	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459	06/2015	845.24 -	941.00	859.59	- -	01/2020	11.33
339	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482	08/2015	814.04 -	825.17	646.72	- -	-	1.37
340	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492	11/2015	867.66 -	1,464.24	1,255.55	05/2018 -	-	68.76
341	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494	05/2013	1,055.00 -	1,601.77	1,393.40	11/2015 -	-	51.83
342	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503	10/2015	447.29 -	746.43	614.07	12/2017 -	06/2020	66.88
343	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506	01/1991	642.41 -	681.67	402.94	- -	10/2020	6.11

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
344	MEERUT-BULANDSHAHAHAR - [N24000539]	01/2016	683.24 -	987.94	727.69	- -	02/2020	44.60
345	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]	03/2016	1,587.49 -	2,982.00	276.87	04/2019 -	-	87.84
346	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]	05/2016	364.56 -	392.00	286.99	- -	08/2020	7.53
347	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]	08/2016	1,388.34 -	2,587.50	1,449.00	09/2019 -	03/2020	86.37
348	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]	09/2016	950.69 -	1,108.00	1,399.33	08/2019 -	12/2020	16.55
349	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]	09/2016	1,100.19 -	1,145.31	1,045.00	- -	05/2020	4.10
350	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]	11/2016	290.73 -	315.00	246.70	- -	03/2020	8.35
351	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]	11/2012	605.84 -	722.46	722.46	07/2018 -	02/2020	19.25
352	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	03/2017	1,184.71 -	1,310.00	563.15	03/2020 -	08/2020	10.58
353	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	03/2017	744.64 -	982.00	-	03/2020 -	03/2020	31.88
354	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	03/2017	1,030.44 -	1,065.51	1,015.76	03/2020 -	05/2020	3.40
355	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	03/2017	988.34 -	1,043.28	1,035.00	03/2020 -	08/2020	5.56
356	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]	03/2017	1,059.73 -	1,071.00	610.87	03/2017 -	11/2020	1.06
357	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]	03/2017	1,098.06 -	1,160.64	1,068.76	03/2020 -	08/2020	5.70
358	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	03/2017	754.54 -	756.27	193.96	03/2020 -	08/2021	.23
359	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	03/2017	672.89 -	736.01	-	03/2020 -	03/2020	9.38
360	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]	03/2017	1,041.62 -	1,187.10	829.16	03/2020 -	05/2020	13.97
361	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]	03/2017	165.50 -	172.16	117.09	03/2020 -	03/2020	4.02
362	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]	03/2017	1,288.07 -	1,420.00	532.31	03/2020 -	03/2021	10.24

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
363	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 -	2,447.00	2,029.34	03/2020 -	06/2020	18.50
364	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 -	1,177.00	702.31	03/2020 -	07/2020	41.54
365	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O) - [N24000675	03/2017	993.16 -	1,434.00	765.31	03/2020 -	06/2020	44.39
366	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691	04/2017	894.00 -	929.32	760.00	04/2020 -	04/2020	3.95
367	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693	06/2017	1,958.88 -	1,993.81	1,116.85	06/2020 -	02/2021	1.78
368	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704	09/2017	1,124.11 -	1,232.76	314.14	09/2017 -	05/2021	9.67
369	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713	12/2017	404.94 -	448.18	193.77	-	10/2020	10.68
370	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784	02/2018	1,424.77 -	1,853.42	14.19	-	-	30.09
371	SIX-LANING OF BANGALORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787	02/2018	1,995.34 -	2,400.00	1,740.36	-	11/2021	20.28
372	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789	02/2018	2,177.80 -	2,450.00	931.86	-	-	12.50
373	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793	03/2018	925.40 -	1,197.00	563.83	-	-	29.35
374	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800	03/2018	1,120.57 -	1,332.00	510.96	-	-	18.87
375	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801	02/2018	1,052.21 -	1,449.00	342.39	-	01/2021	37.71
376	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807	03/2018	1,532.62 -	2,499.00	730.93	03/2021 -	04/2021	63.05
377	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814	03/2018	1,029.96 -	1,261.05	97.55	-	03/2021	22.44
378	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829	03/2018	1,016.92 -	1,071.00	-	-	04/2021	5.32
379	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830	03/2018	2,065.96 -	2,169.00	-	-	-	4.99

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
380	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831	03/2018	1,294.47 -	1,296.00	-	-	-	.12
381	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839	03/2018	634.70 -	931.21	143.54	-	07/2021	46.72
382	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841	03/2018	795.50 -	799.30	128.56	-	07/2021	.48
383	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853	03/2018	642.13 -	807.00	395.79	-	12/2020	25.68
	Total		73,726.80 -	94,589.63	59,634.73			
	<u>SHIPPING AND PORTS</u>							
	<u>Inland Waterways Authority Of India</u>							
384	JAL MARG VIKAS PROJECT - [N25000072	01/2018	4,200.00 -	5,369.18	1,540.69	03/2023	03/2023	27.84
	Total		4,200.00 -	5,369.18	1,540.69			
	<u>STEEL</u>							
	<u>National Mineral Development Corporation (Nmhc)</u>							
385	NMDC INTEGRATED STEEL PLANT - [N12000086	01/2010	15,525.00 -	23,140.00	16,468.33	05/2015	07/2020	49.05
	Total		15,525.00 -	23,140.00	16,468.33			
	<u>TELECOMMUNICATIONS</u>							
	<u>Bharat Sanchar Nigam Limited</u>							
386	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113	01/2018	231.80 -	240.10	119.92	10/2018	02/2020	3.58
	<u>Department Of Telecommunication</u>							
387	NETWORK FOR SPECTRUM - [N26000101	03/2012	13,334.00 -	24,664.00	12,146.00	07/2015	05/2020	84.97
	Total		13,565.80 -	24,904.10	12,265.92			
	<u>URBAN DEVELOPMENT</u>							
	<u>Central Public Works Department</u>							
388	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088	02/2014	388.00 -	490.00	442.51	05/2017	03/2020	26.29

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
389	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 -	2,000.00	436.20	10/2019 -	03/2021	64.04
390	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100	02/2016	496.18 496.00	498.99	118.00	06/2017 -	03/2021	.57
391	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101	12/2008	114.26 266.00	266.00	-	12/2013 -	-	132.80
392	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102	08/2016	294.00 -	350.69	219.60	04/2019 -	05/2020	19.28
393	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119	12/2016	549.31 -	559.47	373.45	07/2019 -	08/2020	1.85
<u>Chennai Metro Rail Ltd</u>								
394	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084	02/2009	14,600.00 -	19,058.00	16,352.87	12/2015 -	-	30.53
<u>Hindustan Steelwork Construction Limited</u>								
395	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099	12/2007	202.61 227.00	227.00	199.95	12/2016 -	-	12.04
396	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100	10/2011	175.49 206.71	206.71	141.28	12/2016 -	-	17.79
397	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101	05/2005	768.88 1,070.97	1,113.34	1,085.64	02/2014 -	-	44.80
398	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098	03/2007	149.73 173.00	175.94	176.65	12/2015 -	-	17.50
<u>Kochi Metro Rail Corporation Ltd</u>								
399	KOCHI METRO RAIL PROJECT - [N28000081	07/2012	5,181.79 -	6,218.14	5,817.11	07/2017 -	03/2020	20.00
<u>National Building Construcion Corporation Ltd</u>								
400	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080	06/2012	4,264.00 -	4,720.73	4,553.13	11/2019 -	05/2020	10.71
	Total		28,403.46 -	35,885.01	29,916.39			
<u>WATER RESOURCES</u>								
<u>Polavaram Project Authority</u>								
401	POLAVARAM IRRIGATION PROJECT - [N30000002	02/2009	10,151.04 -	55,548.87	32,535.80	03/2020 -	12/2021	447.22
	Total		10,151.04 -	55,548.87	32,535.80			

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2020)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
	Grand Total		6,24,664.33	10,49,277.66	579,951.05			

Details of Delayed Projects w.r.t. Original Schedule

Annexure - VI

Costing Rs. 150 Crore and above (January 2020)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
	<u>Bhavini Limited</u>									
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI, TAMIL NADU	09/2003	3,492.00 5,677.00	6,840.00	5,862.38	09/2010 09/2016	10/2021	133	95.88	NIL
	<u>Nuclear Power Corporation Of India Limited</u>									
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 -	16,580.00	14,629.00	12/2015 -	09/2021	69	44.69	
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 -	17,079.00	11,737.00	12/2016 -	03/2023	75	38.63	
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL, TAMIL NADU	03/2013	39,849.00 -	39,849.00	17,987.00	11/2020 -	11/2023	36	0	
	Total		67,120.00 -	80,348.00	50,215.38					
	<u>CIVIL AVIATION</u>									
	<u>Airport Authority Of India Limited</u>									
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, A & N ISLANDS	10/2013	314.61 -	441.33	85.79	09/2018 -	06/2020	21	40.28	
6	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPORT - [N04000076]AAI, DELHI	11/2016	233.38 -	233.38	84.73	04/2020 -	12/2020	8	0	
7	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA - [N04000080]AAI, WEST BENGAL	01/2016	219.91 -	219.91	65.45	03/2020 -	12/2020	9	0	
8	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI - [N04000074]AAI, TAMIL NADU	06/2018	2,467.00 -	2,467.00	213.17	02/2022 -	08/2022	6	0	
	Total		3,234.90 -	3,361.62	449.14					
	<u>COAL</u>									
	<u>Bharat Coking Coal Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
9	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	269.82	181.30	04/2014 -	03/2020	71	0	
10	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	289.45	263.37	05/2014 03/2020	05/2020	72	0	
11	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	414.42	04/2015 04/2022	04/2022	84	0	
	<u>Central Coal Fields Limited</u>									
12	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	107.16	03/2011 -	03/2021	120	0	
13	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	181.17	03/2012 -	03/2021	108	0	
14	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	399.09	03/2016 -	03/2021	60	0	
15	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	90.75	03/2014 -	03/2021	84	0	
16	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	706.40 -	706.40	501.09	07/2012 -	03/2022	116	0	
	<u>Eastern Coal Fields Limited</u>									
17	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05 -	1,055.05	562.60	03/2018 -	10/2020	31	0	1. Rehabilitation of PAFs: Progress of R&R activity delayed due to disputes among villagers for selection of rehab. site and resistance by villagers in shifting. 2.Expediting the work of tree felling for hand over of 32.65 Ha forest land.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
18	RANIGANJ MASTER PLAN - [N06000163]ECL, WEST BENGAL	08/2009	2,661.73	5,146.48	364.72	08/2019	08/2024	60	93.35	i). Publication of Demographic survey report for non-ECL households by ADDA. ii). Publication of valuation report by ADDA against immovable properties for LTH households to assess the financial impact for payment of cash compensation. As per decision taken by WB Govt. publication of survey report will be done as and when construction of bulk chunk of flats at rehabilitation sites are completed. iii). Identification of balance 85.29 Ha land in non- coal bearing measures for construction of balance 17928 flats. As per resolution of review meeting taken by Sec(coal), CMPDI, RI-1 has identified land areas both in non-coal bearing and deep-seated coal bearing measures and report was sent to ADDA for utilization in rehabilitation purpose. WB Govt. is now examining the encumbrance free land areas. Further communication in this regard is yet to be received from State authority. v). Delay in taking over permissive possession of 4.83 acres ECL land in connection with construction of rehabilitation townships. ADDA requested IC&E Deptt. Govt. of WB on 07.5.19 to accord approval for taking over permissive possession of ECL land, pending execution of deed conveyance. However, communication in this regard is yet to be received. vi). Consideration of WB Govt. vested land areas below 25 acres for construction purposes, where NOC was accorded on the basis of study and evaluation made by CMPDI, RI-1. Accordingly, ADDA requested IC&E Deptt. to take up the matter at
					243					

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>Mahanadi Coal Fields Limited</u>									
19	KULDA OCP (MAHANADI COALFIELDS LTD) - [N060100092]MCL, ODISHA	01/2005	302.96 -	302.96	270.32	03/2010 -	03/2020	120	0	
20	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL, ODISHA	12/2007	490.10 -	490.10	524.33	03/2017 -	03/2021	48	0	
21	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL, ODISHA	08/2008	207.28 -	207.28	306.94	03/2012 -	03/2021	108	0	
22	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL, ODISHA	05/2014	337.66 -	337.66	215.55	03/2019 -	03/2021	24	0	
23	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL, ODISHA	06/2014	289.03 -	289.03	-	03/2018 -	03/2021	36	0	
24	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL, ODISHA	12/2007	457.77 -	457.77	568.14	03/2013 -	03/2022	108	0	
25	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]MCL, ODISHA	12/2007	172.08 -	172.08	377.07	03/2010 -	03/2022	144	0	
26	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.53 -	479.53	445.05	03/2013 -	03/2022	108	0	
27	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL, ODISHA	05/2014	479.15 -	479.15	214.07	03/2019 -	03/2024	60	0	
	<u>Neyveli Lignite Corporation</u>									
28	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC, TAMIL NADU	06/2011	5,907.11 7,080.41	7,080.41	6,954.15	12/2015 -	03/2020	51	19.86	
	<u>Singareni Colliers Company Limited</u>									
29	RKP OCP PHASE-I - [N06000079]SCCL, TELANGANA	03/2010	209.78 -	209.78	137.06	03/2015 -	03/2020	60	0	
30	RG OC -III EXTENSION (PHASE - II) PROJECT - [N06000100]SCCL, TELANGANA	06/2012	365.01 -	365.01	171.06	06/2015 -	03/2020	57	0	
31	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL, TELANGANA	07/2012	417.33 -	384.32	115.04	07/2016 -	03/2020	44	-7.91	
32	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL, TELANGANA	11/2012	430.45 -	415.37	189.54	03/2016 -	03/2020	48	-3.5	
33	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]SCCL, TELANGANA	05/2015	397.09 -	442.42	99.56	03/2019 -	03/2020	12	11.42	
34	KOYAGUDEM OPENCAST PROJECT - [N06000146]SCCL, TELANGANA	10/2015	426.79 -	426.79	.72	03/2018 -	03/2020	24	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(January 2020)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
35	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29 -	164.04	120.31	03/2015 -	03/2021	72	-32.3	
36	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL, TELANGANA	07/2011	162.76 -	349.28	12.27	03/2015 -	03/2021	72	114.6	
37	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL, TELANGANA	07/2011	447.06 -	473.22	18.60	03/2015 -	03/2021	72	5.85	
38	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]SCCL, TELANGANA	03/2017	413.84 -	413.84	123.18	03/2019 -	03/2022	36	0	
39	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL, TELANGANA	12/2009	418.97 -	489.62	416.88	03/2012 -	03/2023	132	16.86	
40	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL, TELANGANA	10/2006	249.03 -	448.86	326.69	03/2012 -	03/2024	144	80.24	
	<u>South-Eastern Coal Fields Limited</u>									
41	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL, CHHATISGARH	09/2008	152.43 459.49	459.49	195.34	03/2015 03/2020	03/2020	60	201.44	
42	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH	07/2008	178.44 -	178.44	2.92	03/2014 -	03/2020	72	0	
43	BAROUD OC EXPANSION (RCE)-3MTY - [N06000099]SECL, CHHATISGARH	04/2012	258.56 -	258.56	182.04	03/2016 -	03/2020	48	0	
44	AMERA OC RCE - [N06000123]SECL, CHHATISGARH	02/2015	335.97 -	335.97	51.21	03/2018 -	03/2020	24	0	
45	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH	12/2009	321.50 -	321.50	197.36	03/2014 -	03/2021	84	0	
	<u>Western Coal Fields Limited</u>									
46	ADASA UG TO OC - [N06000133]WCL, MAHARASHTRA	08/2015	288.90 -	333.43	38.82	03/2023 -	03/2024	12	15.41	
47	KAMPTEE DEEP OC MINE - [N06000141]WCL, MAHARASHTRA	11/2015	277.65 -	313.34	118.18	03/2021 -	03/2024	36	12.85	
	Total		22,430.74 -	26,878.22	15,458.07					
	<u>FERTILISERS</u>									
	<u>National Fertiliser Limited</u>									
48	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]NFL, PUNJAB	01/2018	218.83 -	218.83	142.01	11/2019 -	05/2020	6	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
49	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]NFL,PUNJAB	01/2018	239.81 -	239.81	156.70	11/2019 -	05/2020	6	0	
	Total		458.64 -	458.64	298.71					
	<u>MINES</u>									
	<u>National Aluminum Company Limited (Nalco)</u>									
50	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]NALCO,TAMIL NADU	09/2017	166.62 163.17	163.17	135.00	06/2019 12/2020	12/2020	18	-2.07	
51	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]NALCO,ODISHA	12/2014	5,540.00 5,540.00	5,540.00	131.22	04/2021 12/2022	12/2022	20	0	
	Total		5,706.62 -	5,703.17	266.22					
	<u>STEEL</u>									
	<u>National Mineral Development Corporation (Nmhc)</u>									
52	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH	01/2010	15,525.00 23,140.00	23,140.00	16,468.33	05/2015 07/2020	07/2020	62	49.05	
	<u>Rastrya Ispat Nigam Limited</u>									
53	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH	04/2014	1,682.85 -	1,682.85	1,341.85	09/2018 02/2020	02/2020	17	0	No
54	CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH	08/2015	320.66 -	320.66	257.04	08/2018 02/2020	02/2020	18	0	NO
55	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH	12/2011	2,858.00 -	2,500.00	1,535.76	12/2017 03/2020	03/2020	27	-12.53	No
	<u>Steel Authority Of India Limited (Sail)</u>									
56	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA	04/2015	3,127.30 -	3,127.30	3,201.42	04/2018 01/2020	01/2020	21	0	
57	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND	05/2015	1,154.18 -	1,154.18	998.53	12/2017 01/2020	03/2020	27	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
58	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	1,034.01	450.11	10/2017 06/2020	06/2020	32	0	
59	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND	11/2016	262.87 -	262.87	131.30	06/2019 06/2020	11/2020	17	0	
	Total		25,964.87 -	33,221.87	24,384.34					
	<u>PETROLEUM</u>									
	<u>Bharat Petroleum Corporation Limited</u>									
60	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL,WEST BENGAL	03/2015	694.00 1,097.54	1,097.54	856.34	10/2018 02/2020	02/2020	16	58.15	
61	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA	11/2014	4,588.29 5,245.96	5,245.96	4,137.20	08/2018 11/2019	02/2020	18	14.33	
62	MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL,MAHARASHTRA	04/2013	449.58 -	449.58	215.10	12/2019 07/2020	07/2020	7	0	
63	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA	02/2016	3,313.00 3,288.96	3,288.96	1,673.55	02/2020 10/2020	10/2020	8	-73	
64	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 -	678.00	8.10	02/2017 -	10/2021	56	0	
65	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA	12/2015	1,112.00 1,507.24	1,507.24	566.00	06/2019 02/2022	02/2022	32	35.54	
	<u>Chennai Petroleum Corporation Limited</u>									
66	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU	09/2017	1,858.00 -	1,858.00	1,229.51	12/2019 -	04/2020	4	0	
67	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU	08/2017	421.00 -	421.00	177.80	08/2020 -	02/2021	6	0	
	<u>Gas Authority Of India Limited</u>									
68	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT	04/2016	327.78 -	200.00	155.59	04/2018 -	02/2020	22	-38.98	
69	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]GAIL,HARYANA	08/2018	286.42 -	286.42	6.18	08/2020 09/2020	09/2020	1	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
70	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE	06/2009	2,915.00 4,915.00	4,915.00	2,784.58	12/2012 02/2022	02/2022	110	68.61	
	<u>Hindustan Petroleum Corporation Limited</u>									
71	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA	06/2017	249.26 -	249.26	62.55	06/2020 -	09/2021	15	0	
72	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]HPCL,JHARKHAND	06/2017	161.50 -	161.50	17.78	06/2020 -	09/2021	15	0	
73	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH	07/2016	20,928.00 26,264.00	26,264.00	8,584.07	07/2020 07/2022	07/2022	24	25.5	
	<u>Indian Oil Corporation Limited</u>									
74	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]IOCL,UTTAR PRADESH	01/2018	666.64 -	666.64	493.90	09/2019 -	01/2020	4	0	
75	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]IOCL,ASSAM	02/2016	2,582.00 -	2,582.00	1,704.47	11/2019 -	02/2020	3	0	
76	BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]IOCL,GUJARAT	03/2018	3,380.00 -	3,380.00	2,346.62	09/2019 -	02/2020	5	0	
77	BS-VI PROJECT AT BONGAIGAON REFINERY - [N16000320]IOCL,ASSAM	05/2018	1,222.00 -	1,222.00	739.04	09/2019 -	02/2020	5	0	
78	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY - [N16000322]IOCL,WEST BENGAL	05/2018	2,934.40 -	2,934.40	1,928.10	09/2019 -	02/2020	5	0	
79	BS-VI PROJECT AT PANIPAT REFINERY - [N16000325]IOCL,HARYANA	12/2017	3,529.00 -	3,529.00	2,088.18	07/2019 -	02/2020	7	0	
80	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]IOCL,ASSAM	08/2018	557.00 -	557.00	313.62	02/2020 -	04/2020	2	0	
81	FUEL QUALITY UPGRADATION (NSU,NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY - [N16000348]IOCL,BIHAR	06/2017	951.64 -	951.64	552.00	10/2019 -	05/2020	7	0	
82	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]IOCL,ODISHA	05/2016	429.00 -	429.00	329.59	01/2019 -	06/2020	17	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
83	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00	690.00	351.04	07/2018	10/2020	27	0	
84	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND	02/2017	160.10	160.10	54.94	02/2020	10/2020	8	0	
85	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]IOCL,MADHYA PRADESH	08/2017	236.00	236.00	49.62	06/2020	10/2020	4	0	
86	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT	10/2017	906.00	906.00	123.94	02/2020	10/2020	8	0	
87	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM	06/2016	423.00	423.00	363.66	08/2019	12/2020	16	0	
88	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]IOCL,HARYANA	04/2018	206.63	206.63	29.25	02/2020	12/2020	10	0	
89	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]IOCL,HARYANA	10/2018	598.00	598.00	27.18	02/2020	01/2021	11	0	
90	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU	05/2016	4,497.00 6,025.00	6,025.00	1,588.02	12/2018	02/2021	26	33.98	
91	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL, WEST BENGAL	04/2017	163.02	163.02	59.14	04/2020	03/2021	11	0	
92	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00	212.00	57.97	01/2021	04/2021	3	0	
93	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA	12/2016	161.59	161.59	40.21	12/2019	07/2021	19	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
94	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH	08/2018	466.00 -	466.00	124.36	04/2021 -	07/2021	3	0	
95	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	466.43	68.41	10/2020 -	08/2021	10	0	
96	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]IOCL,HARYANA	01/2019	909.00 -	909.00	23.71	01/2021 -	08/2021	7	0	
97	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 -	348.00	101.41	01/2021 -	10/2021	9	0	
98	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	318.80	63.90	08/2021 -	11/2021	3	0	
99	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	355.00	29.38	04/2022 -	02/2023	10	0	
100	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA	12/2018	611.00 -	611.00	13.32	04/2022 -	03/2023	11	0	
	<u>Mangalore Refinery And Petrochemicals Limited</u>									
101	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA	11/2017	581.00 -	621.00	154.66	03/2020 11/2020	11/2020	8	6.88	
102	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA	09/2016	1,810.00 1,810.00	1,810.00	1,022.88	12/2019 07/2020	03/2021	15	0	
	<u>Oil & Natural Gas Corporation Limited</u>									
103	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 -	1,683.06	1,386.15	05/2013 02/2020	02/2020	81	95.3	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
104	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	1,933.09	03/2015 03/2020	03/2020	60	29.42	
105	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA	11/2014	6,068.80 -	5,296.93	4,845.91	04/2019 03/2020	03/2020	11	-12.72	
106	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI	08/2014	6,086.08 5,842.31	5,842.31	4,784.88	05/2019 03/2020	03/2020	10	-4.01	
107	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]ONGC,MAHARASHTRA	01/2015	4,619.94 -	4,619.94	4,586.11	12/2017 03/2020	03/2020	27	0	
108	DEVELOPMENT OF B-147 FIELD - [N16000292]ONGC,MAHARASHTRA	02/2017	546.15 565.15	565.15	468.71	11/2019 03/2020	03/2020	4	3.48	
109	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) - [N16000335]ONGC,MAHARASHTRA	04/2018	766.37 -	766.37	481.94	12/2019 03/2020	03/2020	3	0	
110	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA	08/2015	2,818.88 -	2,818.88	2,401.67	03/2019 05/2020	05/2020	14	0	
111	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA	12/2015	3,190.69 -	3,247.19	2,369.08	04/2018 05/2020	05/2020	25	1.77	
112	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	650.82 -	650.82	432.28	03/2019 05/2020	05/2020	14	0	
113	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]ONGC,MAHARASHTRA	02/2019	3,660.71 3,740.05	3,740.05	373.79	04/2021 -	05/2021	1	2.17	
114	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH	03/2016	34,012.00 -	34,012.00	4,995.31	06/2020 -	08/2021	14	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(January 2020)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
115	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]ONGC,MAHARASHTRA	02/2017	4,006.83 -	4,475.92	2,975.26	05/2021 12/2021	12/2021	7	11.71	
116	HEERA REDEVELOPMENT - PHASE III - [N16000360]ONGC,MAHARASHTRA	05/2019	2,494.68 -	2,494.68	270.26	12/2021 -	03/2022	3	0	
	<u>Oil India Limited</u>									
117	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	438.84	268.45	03/2017 06/2020	06/2020	39	24.47	
118	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE	09/2016	571.66 -	571.66	372.70	12/2019 06/2020	06/2020	6	0	
119	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM	01/2018	543.91 -	682.90	71.46	02/2020 -	06/2020	4	25.55	
	Total		1,41,663.58 -	1,53,133.06	68,333.92					
	<u>POWER</u>									
	<u>National Hydro-Electric Power Corporation</u>									
120	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	9,997.11	7,761.19	09/2009 12/2021	12/2021	147	155.05	
121	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	19,496.34	11,842.12	09/2010 08/2023	08/2023	155	210.19	
	<u>National Thermal Power Corporation</u>									
122	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC,MADHYA PRADESH	03/2015	9,870.51 -	11,148.86	9,430.15	01/2020 -	02/2020	1	12.95	
123	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	12/2012	11,846.00 -	12,739.82	12,826.56	10/2017 03/2020	03/2020	29	7.55	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
124	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	03/2013	11,638.55 -	12,865.92	12,503.29	01/2018 03/2020	03/2020	26	10.55	
125	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	12,176.28	10,103.00	02/2017 06/2020	06/2020	40	24.87	
126	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA	02/2014	12,532.44 -	13,740.53	10,182.96	12/2018 02/2020	08/2020	20	9.64	
127	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC,ODISHA	05/2016	1,885.13 -	1,885.13	1,486.29	12/2018 -	08/2020	20	0	
128	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC,WEST BENGAL	12/2016	529.68 -	529.68	294.18	11/2018 -	08/2020	21	0	
129	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH	09/2014	9,188.98 -	10,016.10	7,036.74	07/2019 03/2020	09/2020	14	9	
130	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 7,998.00	9,583.00	8,056.25	07/2012 -	09/2020	98	79.02	
131	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 17,304.00	17,304.00	14,367.00	05/2018 12/2021	06/2021	37	33.47	
132	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 21,312.11	21,312.11	16,928.07	10/2011 08/2021	08/2021	118	145.16	
133	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA	01/2016	10,598.98 -	10,598.98	6,325.54	11/2020 02/2021	09/2021	10	0	
134	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 5,867.38	5,867.38	4,346.71	03/2013 12/2020	12/2021	105	96.99	
135	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 -	15,164.05	9,965.78	06/2019 09/2019	03/2022	33	5.55	
136	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL	09/2014	1,381.84 -	1,592.34	526.08	09/2019 02/2022	11/2022	38	15.23	
	<u>North East Electric Power Corporation</u>									
137	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 7,927.34	7,927.34	7,743.76	12/2009 06/2020	06/2020	126	217.49	
	<u>Power Grid Corporation Of India Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
138	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 260.03	260.03	200.16	07/2017 06/2019	01/2020	30	27.92	
139	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL, WEST BENGAL	04/2016	454.11 -	454.11	297.68	04/2018 01/2020	01/2020	21	0	
140	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE	10/2016	608.24 -	608.24	425.04	04/2019 -	01/2020	9	0	
141	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE	12/2015	3,654.00 -	3,654.00	3,508.04	04/2019 -	01/2020	9	0	
142	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 639.46	639.46	590.30	06/2014 09/2019	02/2020	68	31.17	
143	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 1,891.41	1,891.41	1,283.60	04/2016 08/2019	02/2020	46	38.61	Severe ROW problem at Rajarhat area due to protest by political groups.
144	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE	05/2016	3,519.59 -	3,519.59	2,562.41	05/2019 -	02/2020	9	0	
145	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE	09/2017	198.49 -	198.49	126.26	09/2019 02/2020	02/2020	5	0	
146	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 5,071.94	5,071.94	4,595.36	10/2012 12/2019	03/2020	89	5.14	
147	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 374.63	374.63	224.83	04/2016 12/2017	03/2020	47	0	
148	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 546.36	546.36	470.71	11/2016 06/2020	03/2020	40	4.61	
149	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 5,151.37	5,151.37	3,269.93	03/2018 12/2019	03/2020	24	0	
150	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE	01/2015	871.62 -	871.62	606.81	10/2017 09/2019	03/2020	29	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
151	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 197.40	197.40	85.34	03/2018 -	03/2020	24	0	
152	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	1,394.52	457.17	05/2017 06/2019	03/2020	34	0	
153	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	808.63	547.80	01/2018 03/2020	03/2020	26	0	
154	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE	05/2016	14,733.37 -	14,733.37	9,883.31	11/2019 -	03/2020	4	0	
155	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE	10/2016	408.46 -	408.46	322.79	01/2019 09/2019	03/2020	14	0	
156	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE	02/2017	322.30 -	322.30	166.84	02/2019 04/2020	03/2020	13	0	Court case in 04 location in view of ROW which is hampering progress. Court hearing postponed & now scheduled on 27.01.2020
157	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	235.53	138.98	06/2019 -	03/2020	9	0	
158	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE	03/2017	379.95 -	379.95	113.54	12/2019 -	03/2020	3	0	
159	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT	05/2017	175.64 -	175.64	106.20	09/2018 03/2020	03/2020	18	0	
160	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 -	186.17	111.47	07/2019 -	03/2020	8	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
161	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL, GUJARAT	12/2017	193.14 -	193.14	102.44	06/2019 03/2020	03/2020	9	0	
162	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL, KARNATAKA	05/2017	445.89 -	445.89	332.46	02/2019 12/2019	05/2020	15	0	
163	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL, MULTI STATE	08/2017	1,931.39 -	1,931.39	1,164.36	02/2020 -	06/2020	4	0	Efforts are being made to resolve the issue with the help of Distt. Admin.
164	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL, MULTI STATE	12/2014	4,754.42 -	9,072.36	1,402.48	12/2018 -	12/2020	24	90.82	
165	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL, MULTI STATE	12/2014	5,111.33 -	6,880.36	1,886.30	12/2018 -	12/2020	24	34.61	
166	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL, MULTI STATE	02/2009	11,130.19 14,719.10	14,719.10	12,824.45	08/2013 03/2022	03/2022	103	32.24	
	<u>Thdc India Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
167	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	4,397.80	1,858.35	06/2013 -	12/2022	114	76.51	1) There are frequent hindrances by local villagers since mobilization of works. Recently in VPHEP there was an agitation/ dharna at TBM and Power House site from 25.11.19 and 28.11.19 respectively by locals. The work could be resumed on 16.12.2019 with the intervention of District Administration. Therefore, continuous support on law & order issues is required from GoUK/ District Administration, Chamoli. 2) Approval of Gadi quarry is pending with District Administration/ GoUK.
	Total		2,03,414.11 -	2,73,668.23	2,01,391.08					
	<u>HEAVY INDUSTRY</u>									
	<u>Bharat Heavy Electricals Limited</u>									
168	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL,DELHI	08/2016	1,554.00 -	1,554.00	716.25	09/2019 -	03/2020	6	0	
	Total		1,554.00 -	1,554.00	716.25					
	<u>HEALTH AND FAMILY WELFARE</u>									
	<u>HIL Infra Tech Services Limited</u>									
169	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	715.06	385.77	04/2020 -	10/2020	6	-8.91	
170	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	557.48	327.76	06/2020 -	10/2020	4	-20.7	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
171	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 -	747.80	137.27	05/2021 08/2021	10/2021	5	-14.54	
	<u>Hospital Services Consultancy Corporation Ltd</u>									
172	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	325.00	304.62	05/2017 -	01/2020	32	10.68	
173	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	177.92	147.31	02/2018 -	03/2020	25	16.33	
174	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	274.19	230.83	03/2019 -	03/2020	12	0	
175	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	272.54	204.08	03/2019 -	03/2020	12	.13	
176	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	270.00	210.75	05/2017 -	06/2020	37	32.07	
177	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	363.99	219.50	05/2018 -	07/2020	26	0	
178	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL	08/2017	355.15 -	355.15	233.51	03/2019 -	07/2020	16	0	
179	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	499.23	337.32	11/2013 -	09/2020	82	20.55	
	Total		4,693.67 -	4,558.36	2,738.72					
	<u>RAILWAYS</u>									
	<u>Central Railways</u>									
180	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 199.12	312.00	293.06	03/2019 03/2020	03/2020	12	69.51	
181	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50 -	4,517.49	2,495.07	03/2021 -	03/2022	12	98.88	
182	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89 -	1,377.48	318.59	03/2021 -	03/2022	12	73.73	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
183	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19 -	1,272.19	339.43	03/2022 -	03/2023	12	0	
184	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02 -	540.02	265.90	03/2022 -	03/2024	24	0	
185	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 -	1,035.16	138.46	03/2022 -	03/2024	24	0	
186	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 -	637.95	76.12	03/2023 -	03/2024	12	0	
	<u>Container Corporation Of India</u>									
187	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	174.00	164.41	03/2019 -	02/2020	11	0	
188	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	493.17	443.19	03/2018 -	03/2020	24	0	
189	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32 -	346.32	292.82	03/2019 -	03/2020	12	0	
190	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	235.00	10.88	03/2019 -	12/2020	21	.21	
	<u>East Central Railways</u>									
191	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	324.73 898.53	1,050.00	1,041.96	03/2012 -	03/2020	96	223.35	
192	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	477.88 751.55	751.55	674.58	03/2012 -	03/2020	96	57.27	
193	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	678.54 678.54	678.54	556.86	03/2019 -	02/2021	23	0	
194	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	681.43	03/2020 -	03/2021	12	0	
195	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	528.57	128.55	03/2019 -	03/2021	24	0	
196	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR	12/2015	1,200.20 1,200.20	1,200.20	586.83	03/2020 -	10/2021	19	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
197	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR	12/2015	1,491.47 -	1,491.47	448.67	03/2020 -	12/2021	21	0	
198	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	548.00 819.01	819.01	525.18	03/2020 -	03/2022	24	49.45	
199	SAGALI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 1,215.54	1,215.54	156.95	03/2021 -	03/2022	12	63.37	
200	MUZAFFARPUR SAGALI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 1,185.73	1,185.73	60.65	03/2021 -	03/2022	12	62.06	
	<u>East Coast Railway</u>									
201	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	238.03	205.65	03/2020 -	03/2021	12	52.77	
202	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 1,539.28	1,539.28	972.93	02/2019 03/2022	03/2022	37	38.43	
203	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 701.61	810.02	139.27	11/2018 -	03/2022	40	15.45	
204	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 843.04	843.04	147.39	10/2020 03/2023	03/2023	29	0	
205	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	1,160.00 1,160.83	1,160.83	749.76	03/2020 03/2023	03/2023	36	.07	
206	JAGDALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 1,547.38	1,547.38	435.59	03/2022 03/2023	03/2023	12	0	
207	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 1,172.92	1,172.92	560.36	12/2018 03/2022	03/2023	51	0	
208	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 2,499.71	3,382.95	447.56	03/2022 03/2024	03/2024	24	35.33	
209	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 3,791.66	3,791.66	1,270.24	03/2009 -	06/2024	183	29.71	
210	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 198.07	1,928.07	780.24	06/2021 -	06/2024	36	137.8	
211	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 2,361.74	2,361.74	247.79	03/2022 -	03/2025	36	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>Eastern Railways</u>									
212	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	157.94	51.75	11/2018 -	03/2021	28	0	
213	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	542.18 -	693.80	474.79	03/2020 -	03/2021	12	27.96	State Govt. is requested to deposit Rs.121.24 Crs. for their balance share of cost for the project. But still deposition is awaited.
214	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	1,425.44	637.56	02/2013 -	03/2024	133	134.8	
215	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	1,619.48	872.43	03/2019 12/2009	03/2025	72	36.22	1. Acquisition of land in stretch of 3.126 KM between Kamarpukur and Mayanapur and pending over of 5.679 KM stretch possession to Railway. 2. Villagers of Vill.Bhadadighi, Hooghly District, are not allowing to work over a pond namely .Bhabadighi between Goghat and Kamarpukur . 3. Tarakeswar to Dhaniakhali (19 Km) New line, Arambagh – Irphala (18.3 Km) New line , Irphala – Ghatal (11.2 Km) New line and Arambagh – Champadanga (23.30 Km) New line -- Work could not be started due to non availability of land
216	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	1,106.62 -	1,091.59	877.32	12/2010 12/2017	03/2025	171	-1.36	Govt. of West Bengal to deposit Rs. 238.68 Cr. for their balance share of cost towards project Katwa-BWN G.C.
217	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	545.70	148.49	03/2006 -	03/2025	228	34.08	Land is required for execution of the MM projects

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
218	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	2,137.81	300.18	03/2022 -	03/2025	36	133.39	1. Jharkhand & Bihar Government to expedite land acquisition. Milestones may be set only after physical possession of land. 2. Jharkhand Govt. is to deposit Rs. 159.220Cr. as share of expenditure incurred in this project..
219	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	995.10	507.56	03/2016 -	03/2025	108	7.75	1 Krishnanagar City (Dhubulia) – Charatala (13.00KM) New line, Krishnanagar – Chapra (19.2 KM) New line Work could not be started due to non – availability of land. 2 For Krishnanagar – Nabadwipghat (12.2 KM) Gauge Conversion— (Section Krishnanagar – Amghata) could not be commissioned due to religious structures in alignment and Amghata to Nabadwipghat work is held up due to 41 nos. of un authorized crossings.
220	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.51 -	769.40	103.08	03/2017 -	03/2025	96	29.2	Suri – Prantik New Line (33.90 km). The land acquisition details for 250.627 Hectares, submitted to Govt. of West Bengal.
221	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	266.32	169.37	03/2016 -	03/2025	108	-3.95	For Bira - Chakla (11.50) New line- The work will start after acquisition and handing over of land by State Government.
222	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	296.43	275.76	03/2017 -	03/2025	96	-18.82	Baruipara – Furfura (12.30 km) New line - Work could not be started due to non availability of land.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
223	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	494.59	32.00	03/2005 -	03/2025	240	.01	Budge Budge to Pujali (11.00 km) New Line, Pujali – Uluberia (Birshivpur) (10.25 Km) New Line and Pujali – Bahrahath (9.75 Km) New line-- Work could not be started due to non availability of land
224	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96 -	680.68	159.70	02/2012 -	03/2025	157	36.15	Sangrampur – Krishanchandpur (25 Km) New Line, Diamond Harbour (Gurudasnagar) – Bahrahath (21 Km) New Line and Daimond Harbour (Gurudasnagar) - Kulpi (17.25 Km) New Line: Work could not be started due to non availability of land.
225	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	257.42	108.11	03/2014 -	03/2025	132	0	226.542 acres of land required to be acquired for the MM work.
226	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	108	12.02	
	<u>Indian Railway Construction Company Limited</u>									
227	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON,CHHATISGARH	04/2013	3,055.00 -	3,055.00	2,096.39	09/2018 -	03/2021	30	0	1-Agitation by Land losers.
228	GEVRA ROAD PENDRA ROAD - [N22000488]IRCON,CHHATISGARH	02/2014	2,288.00 -	4,970.11	635.13	03/2022 -	12/2022	9	117.23	
229	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA	04/2016	5,200.00 -	1,700.43	48.00	03/2020 -	06/2023	39	-67.3	
	<u>Metropolitan Rapid Transport Projects</u>									
230	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 1,781.98	2,980.41	1,457.78	03/2004 -	03/2021	204	501.57	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
231	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 -	918.53	284.75	03/2014 -	03/2021	84	-82.67	
232	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	63	75.91	
	<u>North Central Railway</u>									
233	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	2,912.96 -	3,845.60	148.26	03/2022 -	12/2024	33	32.02	
	<u>North East Frontier Railway</u>									
234	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	297.32 -	614.00	275.07	03/2019 -	03/2020	12	106.51	
235	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	385.20 1,532.00	1,532.00	652.15	03/2019 -	03/2020	12	297.72	
236	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 2,145.00	2,145.00	935.62	03/2019 -	03/2020	12	302.54	
237	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	314.00 728.00	728.00	731.27	03/2019 -	03/2020	12	131.85	
238	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	1,180.19 3,300.00	4,541.00	3,346.08	12/2008 -	03/2021	147	284.77	
239	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	569.63 670.00	670.00	82.81	03/2020 09/2021	09/2021	18	17.62	
240	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52 -	5,806.81	876.09	03/2015 -	10/2021	79	149.59	
241	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	4,454.17 13,809.00	12,524.00	9,599.02	03/2011 -	03/2022	132	181.17	
242	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	2,393.47 4,968.00	5,021.45	3,183.01	03/2014 03/2022	03/2022	96	109.8	
	<u>North Eastern Railway</u>									
243	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	477.31	370.93	01/2019 -	01/2020	12	61.8	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
244	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH	04/2017	622.50 427.00	426.74	240.48	04/2017 -	01/2020	33	-31.45	
245	INDARA - DOHRGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	213.35	9.63	04/2016 -	06/2020	50	.16	
246	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	1,028.95	26.06	12/2019 -	04/2021	16	-12.65	
247	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	276.90	-	04/2017 -	04/2022	60	0	
248	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	150.00	-	04/2017 -	10/2022	66	0	
	<u>North Western Railway</u>									
249	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 281.03	410.00	381.92	02/2019 -	02/2020	12	69.36	
250	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	420.18 -	420.18	199.53	03/2020 -	12/2020	9	0	
251	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	303.56	285.01	11/2019 -	12/2020	13	42.26	
252	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	348.55	248.71	12/2019 -	02/2021	14	41.64	
253	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 780.98	886.41	568.73	02/2019 -	06/2021	28	116.16	
254	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	685.99	99.38	03/2020 -	04/2022	25	14.33	
255	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	808.85	81.26	08/2022 -	09/2022	1	0	
	<u>Northern Railway</u>									
256	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 695.00	750.00	290.62	12/2011 -	03/2021	111	161.32	
257	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 -	859.00	835.35	03/2016 -	03/2021	60	37.44	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
258	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	27,949.00	20,501.11	11/2002 -	06/2022	235	1017.96	
259	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE <u>Rail Vikas Nigam Ltd.</u>	03/1981	450.00 2,010.00	2,200.00	668.77	07/2012 -	03/2024	140	388.89	
260	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	1,185.64 -	1,844.47	1,883.44	12/2017 -	03/2020	27	55.57	
261	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	1,200.00	1,209.55	03/2019 -	03/2020	12	29.45	
262	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	396.00	388.21	03/2009 03/2009	06/2020	135	196.83	
263	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	816.55	720.70	03/2016 -	12/2020	57	29.06	
264	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	1,402.02 -	1,100.00	1,122.87	03/2020 -	12/2020	9	-21.54	
265	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	713.48 -	2,300.00	2,131.56	03/2020 -	03/2021	12	222.36	
266	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	948.04 -	1,500.00	1,451.81	03/2020 -	03/2021	12	58.22	
267	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH	04/2011	1,485.85 -	1,485.85	1,196.74	12/2020 -	03/2021	3	0	
268	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70 -	1,202.70	1,008.33	02/2015 -	12/2021	82	0	
269	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,548.66 -	1,548.66	1,421.83	12/2021 -	03/2022	3	0	
270	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	2,200.00	1,966.03	03/2020 -	03/2022	24	46.3	
271	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	1,120.00	1,046.08	03/2019 -	06/2022	39	18.78	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
272	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	1,183.25	1,184.32	12/2020 -	12/2022	24	0	
273	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA	04/2010	2,127.00 -	2,900.00	1,815.11	03/2023 -	03/2024	12	36.34	
274	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60 -	750.56	485.98	03/2022 -	12/2024	33	-20.46	
275	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92 -	1,765.92	674.40	03/2023 -	12/2024	21	0	
276	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	4,724.30	2,307.00	03/2016 -	03/2025	108	19.54	
277	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	4,639.00	871.04	03/2016 -	03/2025	108	59.22	
278	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00 -	16,216.00	1,941.37	12/2024 -	03/2025	3	0	
279	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,733.86	40.13	03/2014 -	12/2025	141	18.95	
	<u>South Central Railway</u>									
280	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 1,780.29	3,472.59	970.69	03/2000 -	03/2021	252	101.54	
281	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA	04/2017	119.73 176.17	449.39	298.13	03/2022 -	12/2022	9	275.34	
282	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 2,120.16	2,120.16	561.18	03/2009 -	03/2023	168	102.85	
283	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	1,160.48 1,160.48	1,160.48	340.48	03/2010 -	03/2023	156	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
284	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 2,063.03	2,063.03	880.17	03/2021 -	03/2023	24	0	
285	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 3,631.00	3,631.00	678.02	03/2022 -	03/2023	12	0	
286	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 1,952.68	1,952.68	329.00	03/2023 -	03/2024	12	5.16	
287	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	2,288.70 2,643.25	2,643.25	860.07	03/2021 -	03/2024	36	15.49	
288	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,132.77 2,132.77	2,132.77	350.17	03/2014 -	03/2024	120	0	
	<u>South East Central Railway</u>									
289	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR,CHHATISGARH	04/2008	872.00 1,226.51	1,226.51	1,066.54	12/2019 03/2020	03/2020	3	40.65	
290	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH	04/2010	585.93 1,268.32	1,268.32	687.95	02/2019 12/2020	12/2020	22	116.46	
291	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	511.86 1,756.00	1,756.00	1,679.29	04/2020 01/2021	01/2021	9	243.06	
292	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA	06/2018	229.00 852.50	852.50	39.69	12/2021 03/2023	03/2023	15	272.27	
293	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATISGARH	04/2015	1,973.00 1,973.64	1,973.64	185.98	03/2021 03/2023	03/2023	24	.03	
294	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH	04/2015	1,370.00 1,370.94	1,370.94	332.76	12/2021 03/2023	03/2023	15	.07	
	<u>South Eastern Railway</u>									
295	RAJKHARSWAN-CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	377.00	183.96	12/2016 08/2018	03/2020	39	153.41	
296	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 358.68	358.68	278.34	12/2018 12/2018	08/2020	20	38.92	
297	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 1,312.96	1,312.96	610.19	03/2020 03/2020	03/2021	12	35.38	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
298	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	1,993.24	469.79	03/2021 03/2021	12/2021	9	15.6	
299	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	651.00 -	1,009.00	7.96	03/2015 03/2025	03/2025	120	54.99	
300	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 1,966.70	2,373.00	485.04	03/2003 03/2030	03/2030	324	130.97	
	<u>South Western Railway</u>									
301	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 644.78	890.00	461.80	03/2017 -	03/2020	36	38.03	
302	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,156.94 1,140.94	1,140.94	918.47	03/2020 -	03/2021	12	-1.38	
303	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 1,870.41	1,870.41	1,056.97	03/2019 -	03/2021	24	15.84	
304	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	986.30 986.30	986.30	303.05	03/2016 -	12/2023	93	0	Land acquisition.
305	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 279.54	279.54	30.62	03/2016 -	12/2023	93	0	
306	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 1,382.78	1,382.78	7.35	03/2002 -	03/2024	264	0	
307	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 832.47	832.47	.94	03/2016 -	03/2024	96	0	GoK has not released any funds to DCs concerned for land acquisition.
308	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 2,841.84	2,841.84	194.25	12/2018 -	12/2024	72	0	land acquisition.
	<u>Southern Railway</u>									
309	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	2,072.50	1,471.60	02/2019 -	02/2020	12	185.98	
310	OMALUR-METTURDAM-DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU	10/2013	187.26 -	231.67	167.12	04/2014 -	03/2020	71	23.72	
311	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	980.00	683.11	03/2020 -	03/2021	12	222.39	
312	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU	02/2015	760.00 -	1,182.31	446.00	03/2020 -	06/2021	15	55.57	
313	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	1,567.00	-	03/2024 -	03/2026	24	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>West Central Railway</u>									
314	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH	08/2016	582.13	1,247.64	228.36	03/2022	09/2022	6	114.32	
315	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66	8,248.50	1,986.78	05/2008	03/2023	178	3230.57	
316	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	424.60	2,909.99	1,975.34	03/2021	03/2023	24	585.35	
317	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH	12/2015	1,763.93	1,762.94	867.52	03/2020	03/2023	36	-06	
318	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH	06/2016	2,478.23	2,478.23	477.93	03/2022	03/2023	12	0	
	<u>Western Railway</u>									
319	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT	02/1991	551.51 809.07	809.07	635.52	03/2019 03/2020	03/2020	12	46.7	
320	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	829.74 1,215.34	1,310.23	1,532.69	03/2020 03/2021	03/2021	12	57.91	
321	DABHOI-CHANDOD (17.07KM) - GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT	04/2017	691.84 663.29	663.29	199.24	03/2020 03/2021	03/2021	12	-4.13	
322	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH	04/2016	700.00 603.69	603.69	146.09	06/2020 06/2021	06/2021	12	-13.76	
323	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 321.62	321.62	125.76	03/2012 03/2022	03/2022	120	1.06	
324	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 858.56	858.96	534.00	03/2019 03/2022	03/2022	36	167.87	
325	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	1,037.15 1,037.15	1,037.15	1,035.89	03/2021 03/2022	03/2022	12	0	
326	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	3,503.69 3,975.22	3,975.22	1,801.98	03/2022 03/2023	03/2023	12	13.46	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
327	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 1,640.04	1,640.04	756.11	03/2022 03/2023	03/2023	12	0	
	Total		1,85,926.71 -	2,81,911.53	1,29,633.62					
	<u>ROAD TRANSPORT AND HIGHWAYS</u>									
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>									
328	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]MoRTH,ANDHRA PRADESH	03/2015	271.45 -	271.45	182.45	10/2015 01/2020	01/2020	51	0	
329	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]MoRTH,ANDHRA PRADESH	10/2015	333.21 -	355.89	294.81	12/2015 01/2020	01/2020	49	6.81	
330	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO - [N24000930]MoRTH,ANDHRA PRADESH	11/2016	378.24 -	378.24	307.17	01/2018 01/2020	01/2020	24	0	
331	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938]MoRTH,ANDHRA PRADESH	03/2018	297.12 294.00	294.12	373.98	07/2018 01/2020	01/2020	18	-1.01	
332	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]MoRTH,ANDHRA PRADESH	01/2017	576.48 -	576.48	237.30	01/2018 12/2020	01/2020	24	0	
333	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH,MADHYA PRADESH	03/2015	511.83 -	511.83	278.88	08/2017 -	02/2020	30	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
334	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU - [N24000936]MoRTH,ANDHRA PRADESH	03/2018	244.95 245.00	244.95	136.22	08/2018 02/2020	02/2020	18	0	
335	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]MoRTH,ANDHRA PRADESH	03/2018	289.67 290.00	289.67	105.02	08/2018 02/2020	02/2020	18	0	
336	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]MoRTH,ANDHRA PRADESH	11/2016	376.25 -	376.25	228.69	08/2017 02/2020	02/2020	30	0	
337	AKKALKOT TO DHUDHNI - [N24001120]MoRTH,MAHARASHTRA	04/2016	211.42 -	211.42	131.85	02/2019 -	02/2020	12	0	
338	REHABILITATION AND UPGRADATION TO 2LPS 81 TO 175 - [N24000895]MoRTH,MADHYA PRADESH	09/2016	287.34 -	287.34	158.05	01/2019 -	03/2020	14	0	
339	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931]MoRTH,ANDHRA PRADESH	11/2016	290.15 -	290.15	73.11	05/2017 03/2020	03/2020	34	0	
340	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932]MoRTH,ANDHRA PRADESH	01/2017	319.28 -	319.28	111.98	08/2017 03/2020	03/2020	31	0	
341	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]MoRTH,ANDHRA PRADESH	02/2017	429.43 -	429.43	255.68	11/2017 03/2020	03/2020	28	0	
342	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934]MoRTH,ANDHRA PRADESH	03/2018	228.32 -	228.32	48.15	08/2018 03/2020	03/2020	19	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
343	REHABILITATION AND UPGRADATION OF HARPALPUR-SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942]MoRTH,UTTAR PRADESH	03/2016	208.50 -	208.50	141.54	11/2019 -	03/2020	4	0	
344	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966]MoRTH,ANDHRA PRADESH	01/2016	348.95 -	348.95	169.46	08/2016 03/2020	03/2020	43	0	
345	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967]MoRTH,ANDHRA PRADESH	03/2016	444.84 -	444.84	273.88	09/2016 03/2020	03/2020	42	0	
346	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA	10/2016	248.83 -	248.83	91.52	03/2019 -	03/2020	12	0	
347	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH,TELANGANA	01/2017	300.00 -	300.00	100.33	05/2019 -	03/2020	10	0	
348	INDAPUR TO VADPALE - [N24001114]MoRTH,MAHARASHTRA	01/2017	1,202.52 1,202.52	1,202.52	635.90	12/2019 -	03/2020	3	0	
349	VADPALE TO BHOGAN KHURD - [N24001115]MoRTH,MAHARASHTRA	01/2017	1,598.47 1,560.00	1,598.47	768.91	11/2019 -	03/2020	4	0	
350	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH,UTTAR PRADESH	03/2016	240.30 240.00	240.30	198.06	01/2020 -	03/2020	2	0	
351	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH - [N24001145]MoRTH,UTTAR PRADESH	05/2013	164.54 165.00	164.54	127.34	08/2015 -	03/2020	55	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
352	REHABILITATION AND UPGRADATION OF TULSIPUR - BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]MoRTH,UTTAR PRADESH	03/2016	249.50 -	249.50	160.60	05/2019 -	03/2020	10	0	
353	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH	03/2018	233.04 -	233.04	131.22	03/2018 -	04/2020	25	0	
354	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH	02/2018	279.44 -	279.44	76.00	03/2018 -	04/2020	25	0	
355	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964]MoRTH,ANDHRA PRADESH	08/2016	350.61 -	350.61	310.25	01/2017 04/2020	04/2020	39	0	
356	KOLHA TO NASRATPUR - [N24001111]MoRTH,MAHARASHTRA	04/2016	281.78 282.00	281.78	29.73	04/2019 -	04/2020	12	0	
357	R AND U FROM KM 385.00 TO KM 420.000 TO 2- LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404 - [N24001205]MoRTH,UTTAR PRADESH	12/2016	209.10 -	209.10	160.28	10/2019 04/2020	04/2020	6	0	
358	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]MoRTH,MADHYA PRADESH	11/2013	497.05 -	881.05	624.54	05/2017 -	05/2020	36	77.26	
359	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH	03/2018	162.56 -	162.56	119.50	03/2018 -	05/2020	26	0	
360	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]MoRTH,MADHYA PRADESH	11/2017	235.91 -	235.91	156.89	02/2018 -	05/2020	27	0	
361	UPGRADATION OF PACHORE-SHUJALPUR ROAD TO 2L + PS - [N24000881]MoRTH,MADHYA PRADESH	11/2017	184.62 -	184.62	76.60	02/2018 -	05/2020	27	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
362	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884]MoRTH,MADHYA PRADESH	03/2018	191.21 -	191.21	78.35	11/2019 -	05/2020	6	0	
363	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]MoRTH,ANDHRA PRADESH	03/2018	504.19 504.00	504.19	248.37	11/2018 05/2020	05/2020	18	0	
364	WAKAN PALI KHOPOLI - [N24001026]MoRTH,MAHARASHTRA	01/2017	376.19 376.19	376.19	37.03	05/2019 -	05/2020	12	0	
365	DEORI TO AMGAON - [N24001032]MoRTH,MAHARASHTRA	01/2017	409.62 410.00	409.62	181.78	05/2019 -	05/2020	12	0	
366	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA	05/2018	171.60 -	171.60	.86	05/2018 -	05/2020	24	0	
367	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH	03/2018	166.21 -	166.21	67.45	08/2018 -	06/2020	22	0	
368	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]MoRTH,MADHYA PRADESH	03/2018	217.22 226.88	226.88	86.83	08/2018 -	06/2020	22	4.45	
369	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH	11/2017	249.05 -	249.05	143.64	07/2018 -	06/2020	23	0	
370	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]MoRTH,HARYANA	01/2017	247.25 -	247.25	144.71	03/2019 06/2020	06/2020	15	0	
371	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA	10/2016	298.32 -	298.32	83.57	02/2019 -	06/2020	16	0	
372	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA	01/2017	391.06 391.00	391.06	147.00	06/2019 -	06/2020	12	0	
373	KARAD TO TAGAON - [N24001053]MoRTH,MAHARASHTRA	01/2017	537.81 538.00	537.81	98.97	06/2019 -	06/2020	12	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
374	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MoRTH,MAHARASHTRA	02/2017	407.19 407.00	407.19	25.00	06/2019 -	06/2020	12	0	
375	MALEWADA TO CHIMUR - [N24001104]MoRTH,MAHARASHTRA	10/2016	322.55 -	322.55	184.91	06/2019 -	06/2020	12	0	
376	PARLI PIMPLA DAHIGUDA - [N24001138]MoRTH,MAHARASHTRA	02/2017	205.72 205.72	205.72	30.42	06/2019 -	06/2020	12	0	
377	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]MoRTH,MIZORAM	08/2010	186.96 -	305.61	279.13	09/2014 06/2020	06/2020	69	63.46	
378	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]MoRTH,UTTAR PRADESH	07/2016	208.88 -	208.88	95.59	10/2019 -	06/2020	8	0	
379	REHABILITATION AND UPGRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH,MADHYA PRADESH	02/2018	169.63 -	169.63	14.67	03/2018 -	07/2020	28	0	
380	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]MoRTH,MADHYA PRADESH	03/2016	877.79 -	877.79	467.48	06/2019 -	07/2020	13	0	
381	REHABILITATION AND UPGRADATION OF KARNATAKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]MoRTH,ANDHRA PRADESH	03/2016	995.09 995.00	995.09	419.22	05/2016 07/2020	07/2020	50	0	
382	MANGAON TO DIGHI PORT - [N24001024]MoRTH,MAHARASHTRA	01/2017	457.52 457.52	457.52	277.98	07/2019 -	07/2020	12	0	
383	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]MoRTH,MADHYA PRADESH	12/2015	957.54 -	957.54	573.28	02/2020 -	08/2020	6	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
384	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALAT JUNCTION) TO KM 420.800(P - [N24000963]MoRTH,ANDHRA PRADESH	01/2018	418.03 -	418.03	194.62	08/2018 08/2020	08/2020	24	0	
385	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH	11/2015	628.45 -	628.45	300.52	01/2020 -	09/2020	8	0	
386	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH	01/2017	205.05 -	205.05	85.57	03/2017 -	09/2020	42	0	
387	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]MoRTH,MADHYA PRADESH	11/2017	254.17 -	254.17	157.83	02/2018 -	09/2020	31	0	
388	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]MoRTH,MADHYA PRADESH	01/2017	373.82 -	373.82	143.05	09/2019 -	09/2020	12	0	
389	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]MoRTH,MADHYA PRADESH	01/2016	809.16 -	809.16	353.90	07/2018 -	09/2020	26	0	
390	WADI TO ASOLA - [N24001022]MoRTH,MAHARASHTRA	01/2017	363.82 363.82	363.82	92.10	09/2019 -	09/2020	12	0	
391	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MoRTH,MADHYA PRADESH	11/2017	392.33 428.55	428.55	253.99	03/2018 -	09/2020	30	9.23	
392	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]MoRTH,MIZORAM	11/2010	624.41 -	992.67	886.01	03/2011 12/2020	12/2020	117	58.98	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
393	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH	03/2018	214.69 -	214.69	30.44	03/2018 -	12/2020	33	0	
394	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH,PUNJAB	10/2017	1,069.59 -	1,069.59	663.50	10/2019 12/2020	12/2020	14	0	
395	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969]MoRTH,ANDHRA PRADESH	01/2017	263.45 -	263.45	60.26	09/2017 12/2020	12/2020	39	0	
396	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]MoRTH,BIHAR	05/2014	199.98 -	199.98	153.43	08/2016 -	12/2020	52	0	
397	BARASGAON TO RAHATEE - [N24001113]MoRTH,MAHARASHTRA	07/2016	289.11 290.00	289.11	33.82	09/2018 -	04/2021	31	0	
398	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH,PUNJAB	03/2018	170.57 192.48	170.57	8.14	11/2020 -	05/2021	6	0	
399	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA	02/2017	157.32 188.00	157.32	-	05/2019 -	05/2021	24	0	
400	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]MoRTH,MIZORAM	08/2010	193.69 -	327.92	258.71	10/2010 06/2021	06/2021	128	69.3	
401	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH,WEST BENGAL	03/2016	160.27 213.97	213.97	20.11	08/2019 -	08/2021	24	33.51	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
402	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH, WEST BENGAL	06/2016	236.78 263.26	263.26	59.92	08/2019 -	08/2021	24	11.18	
403	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]MoRTH, MADHYA PRADESH	11/2011	954.43 1,191.51	1,191.51	235.61	09/2015 -	10/2021	73	24.84	
404	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]MoRTH, MIZORAM	08/2010	195.04 -	377.99	312.41	10/2010 12/2020	06/2020	116	93.8	
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>									
405	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL, ARUNACHAL PRADESH	12/2016	138.93 155.00	155.00	79.91	01/2017 -	01/2020	36	11.57	
406	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL, ARUNACHAL PRADESH	03/2015	394.00 -	394.00	325.08	06/2018 -	03/2020	21	0	
407	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL, NAGALAND	03/2016	373.07 387.00	387.00	216.07	08/2016 -	03/2020	43	3.73	
408	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL, NAGALAND	03/2016	429.52 340.00	340.00	189.88	08/2016 -	03/2020	43	-20.84	
409	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL, NAGALAND	03/2016	396.52 339.55	339.55	237.99	08/2016 -	06/2020	46	-14.37	
410	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL, NAGALAND	02/2017	387.00 -	387.00	145.18	09/2018 -	08/2020	23	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
411	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL, ASSAM	05/2015	454.89 -	454.89	141.83	05/2018 05/2020	12/2020	31	0	
412	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL, ARUNACHAL PRADESH	02/2017	168.32 168.32	168.32	40.78	04/2017 02/2018	02/2021	46	0	
413	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL, ARUNACHAL PRADESH	02/2017	180.57 180.57	180.57	16.80	04/2017 02/2018	02/2021	46	0	
414	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL, ARUNACHAL PRADESH	02/2017	216.71 216.71	216.71	25.17	04/2017 02/2018	02/2021	46	0	
415	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL, ARUNACHAL PRADESH	02/2017	167.28 167.28	167.28	21.54	04/2017 02/2018	02/2021	46	0	
416	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL, ARUNACHAL PRADESH	03/2017	284.09 284.09	284.09	96.13	04/2017 03/2018	03/2021	47	0	
417	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL, ASSAM	01/2016	294.17 -	294.17	76.25	01/2016 02/2019	04/2021	63	0	
418	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL, MANIPUR	08/2017	517.57 -	457.77	137.04	10/2018 -	10/2021	36	-11.55	
419	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL, ASSAM	06/2015	437.39 -	437.39	10.01	06/2018 12/2020	12/2021	42	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
420	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL, ASSAM	06/2015	463.49 -	463.49	26.15	06/2018 01/2021	12/2021	42	0	
421	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL, ARUNACHAL PRADESH	01/2017	1,253.10 -	1,253.10	204.77	03/2017 -	03/2022	60	0	
	<u>National Highways Authority Of India</u>									
422	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI, JHARKHAND	08/2016	323.72 -	323.72	232.58	08/2018 -	01/2020	17	0	
423	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI, MADHYA PRADESH	10/2017	639.97 -	639.97	331.84	10/2017 -	01/2020	27	0	
424	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI, UTTARAKHAND	11/2012	605.84 -	722.46	722.46	07/2018 12/2019	02/2020	19	19.25	
425	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, ASSAM	12/2003	208.00 -	230.00	340.21	04/2008 -	03/2020	143	10.58	
426	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, MULTI STATE	12/2003	604.00 364.59	364.59	237.64	12/2009 08/2020	03/2020	123	-39.64	
427	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, HARYANA	04/2007	486.00 -	486.00	470.01	05/2010 -	03/2020	118	0	
428	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA	05/2009	1,108.00 2,967.50	2,967.50	3,990.72	11/2011 -	03/2020	100	167.82	
429	PUNE-SATARA (NH-4) - [N24000156]NHAI, MAHARASHTRA	10/2010	1,724.55 -	1,724.55	2,442.58	03/2013 -	03/2020	84	0	
430	PATNA-MUZZAFFARPUR - [N24000165]NHAI, BIHAR	08/2010	671.30 -	671.30	1,132.48	02/2013 -	03/2020	85	0	
431	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI, ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	3,260.65	05/2014 12/2019	03/2020	70	0	
432	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, BIHAR	01/2011	575.00 -	575.00	850.24	07/2013 -	03/2020	80	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
433	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 585.00	591.00	571.86	11/2013 12/2019	03/2020	76	15.53	
434	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	1,396.18	2,894.94	09/2014 -	03/2020	66	0	
435	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI, RAJASTHAN	10/2015	597.00 -	597.00	587.64	10/2017 -	03/2020	29	0	
436	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI, MAHARASHTRA	01/2015	972.50 -	972.50	1,492.00	07/2017 12/2019	03/2020	32	0	
437	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI, HIMACHAL PRADESH	09/2015	934.46 -	934.46	586.91	03/2018 -	03/2020	24	0	
438	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI, KARNATAKA	03/2015	1,388.00 -	1,388.00	1,203.00	08/2018 -	03/2020	19	0	
439	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI, MAHARASHTRA	07/2015	1,871.34 67.34	1,871.34	3,544.79	01/2018 12/2018	03/2020	26	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
440	FOUR / SIX LANE OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI, CHHATISGARH	12/2015	726.67 598.13	598.13	414.73	04/2018 03/2020	03/2020	23	-17.69	The CALA, Raipur had submitted Proposal of additional 3A area for 12.6814 Ha (missing Khasra/plot no.) . 3A notification was published in Gazette on 04.07.2018 but CALA, Raipur did not provide revenue/ Khasra map to NHAI inspite of repeated request. In 680m length work was held up due to non-payment of land compensation to land owners, so NHAI has processed the 3D notification for 2.561Ha private land considering urgency at project site without revenue khasra map plan and balance 3D for area 10.1204 Ha was kept in hold due to non-receipt of Revenue Khasra map plan from CALA, Raipur. 3D of 2.561 Ha. land was published on 24.08.2018 . In spite of repeated request to CALA, Raipur has not submitted revenue Khasra map plan showing 12.6814Ha land so the 3A notification dated 04.07.2018 balance area 10.1204Ha has lapsed on 03.07.2019. Some land owners (which land 3A was published on 04.07.2018 but 3D not published due to want of revenue Khasra map plan) have filed writ petition in Bilaspur High Court and Court passed order that land compensation should be paid to land owners within 09 months from the date of order after duly verification of land proposed in the acquisition. The land acquisition map showing RoW width for 25 villages are still not submitted by SDM Raipur & SDM Simga due to which 3A for balance 10.1204Ha of land could not be processed.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
441	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	707.82	381.40	08/2018 -	03/2020	19	0	
442	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	804.97	465.05	06/2018 -	03/2020	21	0	
443	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 2,541.32	2,587.50	1,449.00	09/2019 03/2020	03/2020	6	86.37	
444	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	248.97	249.15	05/2019 -	03/2020	10	0	TBRL Issue: 23.4875 Acres land is not available due to transfer of TBRL land in favour of NHAI. Letter written by NHAI HQ in Apr 2019 to MoRTH to take-up the case with MoD for waiver of land compensation of Rs 31 Cr and to hand over the possession of land. The proposal is pending with MoRTH/MOD.
445	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 2,257.49	667.00	464.05	07/2018 -	04/2020	21	0	
446	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 3,007.86	667.00	549.07	06/2018 -	04/2020	22	0	
447	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	244.27	177.41	09/2017 -	04/2020	31	0	
448	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,195.64	08/2013 -	05/2020	81	0	
449	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 414.00	414.00	543.46	05/2018 05/2020	05/2020	24	-12	
450	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	923.04	767.17	11/2016 -	05/2020	42	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
451	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	641.17	370.82	07/2018 -	05/2020	22	0	
452	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 911.07	904.16	855.25	02/2020 11/2017	05/2020	3	0	
453	4-LANNING OF WARDHA-BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	1,065.51	1,015.76	03/2020 -	05/2020	2	3.4	
454	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 2,602.09	1,989.00	892.35	03/2020 11/2017	05/2020	2	0	
455	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	1,187.10	829.16	03/2020 -	05/2020	2	13.97	
456	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	641.17	370.82	07/2016 -	05/2020	46	0	
457	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,336.07	12/2013 -	06/2020	78	0	
458	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,159.10	03/2014 04/2017	06/2020	75	0	
459	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	2,945.00	2,467.00	04/2015 01/2017	06/2020	62	52.73	
460	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	530.07	556.02	08/2016 -	06/2020	46	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
461	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 41.54	636.24	490.35	05/2018 06/2020	06/2020	25	7.24	
462	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 897.03	897.03	796.56	11/2018 07/2019	06/2020	19	-37	
463	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 2,182.03	815.28	520.89	06/2018 -	06/2020	24	0	
464	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 2,433.38	1,027.53	601.13	06/2018 -	06/2020	24	0	
465	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 746.43	746.43	614.07	12/2017 06/2020	06/2020	30	66.88	
466	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH	03/2017	2,064.99 -	2,447.00	2,029.34	03/2020 06/2020	06/2020	3	18.5	
467	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	1,434.00	765.31	03/2020 -	06/2020	3	44.39	
468	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	2,136.97	1,248.94	12/2018 -	07/2020	19	0	
469	FOUR LANNING OF RAMPUR-KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	899.00	641.51	04/2019 07/2020	07/2020	15	0	
470	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	1,177.00	702.31	03/2020 -	07/2020	4	41.54	
471	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	174.34	225.65	03/2008 -	08/2020	149	-28.84	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
472	DEVELOPMENT OF ADEQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	329.92	06/2013 01/2019	08/2020	86	0	
473	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	478.00	315.11	10/2013 -	08/2020	82	-11	
474	CONSTRUCTION OF ROB – FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI, WEST BENGAL	03/2016	229.37 -	229.37	112.94	11/2018 08/2020	08/2020	21	0	
475	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 870.00	870.00	265.48	03/2019 03/2017	08/2020	17	-25.48	Nil
476	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	1,310.00	563.15	03/2020 -	08/2020	5	10.58	
477	4-LANNING OF YAVATMAL- WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 988.00	1,043.28	1,035.00	03/2020 -	08/2020	5	5.56	
478	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	1,160.64	1,068.76	03/2020 -	08/2020	5	5.7	
479	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH	06/2017	648.33 -	306.00	157.33	06/2017 -	08/2020	38	-52.8	
480	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	1,227.87	387.40	09/2017 -	08/2020	35	0	
481	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	2,913.83	07/2015 12/2019	09/2020	62	0	
482	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	727.00	524.15	05/2018 -	09/2020	28	36.88	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
483	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	504.00	241.74	05/2018 04/2019	09/2020	28	-2	
484	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	1,176.37	207.17	08/2017 -	09/2020	37	0	
485	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	2,898.41	06/2014 09/2017	10/2020	76	0	
486	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	976.79	07/2013 11/2020	11/2020	88	0	
487	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	1,364.18	03/2013 11/2019	11/2020	92	0	
488	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	701.40	29.48	03/2019 -	11/2020	20	0	
489	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	870.00	36.30	03/2019 -	11/2020	20	0	
490	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	1,373.28	571.96	03/2020 -	11/2020	8	0	
491	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	1,071.00	610.87	03/2017 05/2018	11/2020	44	1.06	
492	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	964.17	390.91	10/2017 -	11/2020	37	0	
493	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	1,655.01	1,867.51	08/2016 -	12/2020	52	0	
494	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	2,168.66	704.09	06/2019 -	12/2020	18	0	The Funds disbursement by the state government is very slow. 1040 trees are to be cut from the forest/state land.
495	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	322.09	77.53	04/2018 -	12/2020	32	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
496	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	546.00	269.67	07/2019 12/2020	12/2020	17	0	
497	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	591.66	310.56	07/2019 12/2020	12/2020	17	0	
498	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 1,008.00	1,108.00	1,399.33	08/2019 -	12/2020	16	16.55	
499	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	990.61	397.89	09/2017 -	01/2021	40	0	
500	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	400.25	64.89	03/2019 -	02/2021	23	0	
501	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT	06/2017	1,958.88 1,993.81	1,993.81	1,116.85	06/2020 02/2018	02/2021	8	1.78	
502	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,822.59	08/2013 -	03/2021	91	0	
503	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	2,510.04	358.51	08/2019 -	03/2021	19	0	
504	4-LANNING OF KODEBAD-DHANTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHATTI - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	446.17	38.97	03/2019 -	03/2021	24	0	
505	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	1,420.00	532.31	03/2020 -	03/2021	12	10.24	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
506	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	649.50	155.81	03/2019 04/2021	04/2021	25	0	
507	FOUR LANEING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH	03/2018	1,532.62 2,499.00	2,499.00	730.93	03/2021 -	04/2021	1	63.05	
508	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	227.77	11.00	03/2020 -	05/2021	14	-3.27	
509	4-LANNING OF THALSERRY - MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	1,232.76	314.14	09/2017 -	05/2021	44	9.67	
510	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	476.56	1.49	07/2017 11/2020	06/2021	47	0	
511	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	756.27	193.96	03/2020 -	08/2021	17	.23	
512	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	2,485.93	596.94	06/2020 -	09/2021	15	0	
513	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	950.64	102.51	08/2017 -	02/2022	54	0	
	Total		1,26,706.35 -	1,34,321.29	94,362.10					
	<u>TELECOMMUNICATIONS</u>									
	<u>Bharat Sanchar Nigam Limited</u>									
514	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]BSNL,MAHARASHTRA	01/2018	231.80 240.10	240.10	119.92	10/2018 02/2020	02/2020	16	3.58	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>Department Of Telecommunication</u>									
515	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	24,664.00	12,146.00	07/2015 -	05/2020	58	84.97	
	Total		13,565.80 -	24,904.10	12,265.92					
	<u>URBAN DEVELOPMENT</u>									
	<u>Ahmedabad Metro Rail</u>									
516	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT	11/2014	10,773.00 -	10,773.00	6,532.69	12/2018 -	07/2020	19	0	
	<u>Bangalore Metro Rail Corporation Limited</u>									
517	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA	02/2014	26,405.14 -	26,405.14	499.85	02/2019 -	03/2020	13	0	
	<u>Central Public Works Department</u>									
518	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	159.35	08/2016 -	01/2020	41	0	
519	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	165.23	100.81	10/2012 -	03/2020	89	0	
520	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB	02/2014	388.00 500.18	490.00	442.51	05/2017 -	03/2020	34	26.29	
521	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]CPWD,PUNJAB	08/2016	294.00 350.69	350.69	219.60	04/2019 -	05/2020	13	19.28	
522	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL	10/2014	162.88 179.10	162.88	148.52	04/2018 06/2020	06/2020	26	0	
523	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD,TAMIL NADU	12/2015	209.00 -	209.00	150.71	10/2019 -	07/2020	9	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
524	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI	10/2016	248.20 -	248.20	52.95	04/2018 02/2020	08/2020	28	0	
525	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI	10/2017	271.90 -	271.90	65.00	11/2019 08/2020	08/2020	9	0	
526	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN	12/2016	549.31 559.47	559.47	373.45	07/2019 03/2020	08/2020	13	1.85	
527	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	97.70	03/2016 -	09/2020	54	0	
528	RESIDENTIAL QUATERS FOR HAL, BANGLORE - [N28000103]CPWD,KARNATAKA	12/2016	246.31 -	246.31	85.43	02/2020 -	09/2020	7	0	
529	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR	02/2014	216.69 -	216.69	52.00	03/2015 -	10/2020	67	0	
530	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI	06/2015	197.33 -	197.33	67.09	04/2019 -	12/2020	20	0	Work delayed due to non shifting of JJ Clusters by DUSIB.
531	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]CPWD,MAHARASHTRA	01/2018	223.37 -	223.37	48.89	07/2020 12/2020	12/2020	5	0	
532	CONST OF 152 QTRS. 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT - [N28000139]CPWD,PONDICHERRY	03/2018	195.00 -	195.00	-	09/2020 -	01/2021	4	0	
533	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB - [N28000120]CPWD,PUNJAB	01/2018	430.00 387.83	387.83	124.24	05/2020 -	02/2021	9	-9.81	
534	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	2,000.00	436.20	10/2019 -	03/2021	17	64.04	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
535	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	498.99	118.00	06/2017 -	03/2021	45	.57	
536	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST) - [N28000112]CPWD,KERALA	09/2017	150.29 -	150.29	21.82	03/2020 11/2020	03/2021	12	0	
537	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA	10/2016	209.84 -	209.84	70.43	03/2020 -	05/2021	14	0	
538	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD,ODISHA	01/2019	790.79 -	790.79	41.06	03/2022 06/2022	06/2022	3	0	
	<u>Chennai Metro Rail Ltd</u>									
539	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU	06/2016	3,770.00 -	3,770.00	2,258.91	03/2018 06/2020	06/2020	27	0	
	<u>Hindustan Steelwork Construction Limited</u>									
540	IRRIGATION WORK OF BAGMATI - [N12000108]HSLC,BIHAR	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72	0	
	<u>Kochi Metro Rail Corporation Ltd</u>									
541	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 5,687.79	6,218.14	5,817.11	07/2017 -	03/2020	32	20	
	<u>Maharashtra Metro Rail Corporation Ltd.</u>									
542	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA	12/2016	11,420.00 11,420.00	11,420.00	3,614.06	11/2021 03/2022	03/2022	4	0	
	<u>Mumbai Metro Rail Corporation Ltd</u>									
543	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	05/2020	64	0	
	<u>National Building Construction Corporation Ltd</u>									
544	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI	06/2012	4,264.00 4,720.73	4,720.73	4,553.13	11/2019 03/2020	05/2020	6	10.71	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	Total		92,897.89 -	95,301.25	26,802.72					
	<u>WATER RESOURCES</u>									
	<u>Kolkata Metropolitan Development Authority</u>									
545	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046]KMDA, WEST BENGAL	02/2014	274.76 -	274.76	171.80	12/2019 02/2020	02/2020	2	0	
	<u>Polavaram Project Authority</u>									
546	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA, ANDHRA PRADESH	02/2009	10,151.04 55,548.87	55,548.87	32,535.80	03/2020 11/2019	12/2021	21	447.22	
	<u>Uttar Pradesh Jal Nigam</u>									
547	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA - [N30000011]UP JalNigam, UTTAR PRADESH	02/2017	161.31 -	161.31	37.60	11/2019 02/2020	02/2020	3	0	
548	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020]UP JalNigam, UTTAR PRADESH	02/2011	279.91 -	279.91	199.59	12/2019 03/2020	03/2020	3	0	
	<u>Uttarakhand Pey Jal Nigam</u>									
549	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI - [N30000003]UK JalNigam, UTTARAKHAND	03/2017	273.37 -	273.37	53.19	08/2019 02/2020	02/2020	6	0	
	Total		11,140.39 -	56,538.22	32,997.98					
	<u>COMMERCE AND INDUSTRY</u>									
	<u>Delhi Mumbai Industrial Corridor</u>									
550	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]DMIC, MULTI STATE	09/2011	12,579.09 -	12,579.09	778.93	09/2019 -	09/2020	12	0	
	<u>India International Convention And Expo Centre</u>									
551	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]IICC, DELHI	11/2017	4,773.00 -	5,178.00	1,309.65	12/2019 -	09/2020	9	8.49	
	Total		17,352.09 -	17,757.09	2,088.58					

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (January 2020)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>HUMAN RESOURCE DEVELOPMENT</u>									
	<u>Rail India Technical And Economic Service</u>									
552	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001] RITES, MEGHALAYA	09/2013	484.32 -	626.26	-	09/2014 -	12/2020	75	29.31	
	Total		484.32 -	626.26	.00					
	Grand Total		9,24,314.68	11,94,244.91	6,62,402.75					

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Annexure - VII

(January 2020)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	<u>ATOMIC ENERGY</u>								
	<u>Bhavini Limited</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,840.00	5,862.38	09/2010 -	10/2021	95.88	133
	<u>Nuclear Power Corporation Of India Limited</u>								
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	14,629.00	12/2015 -	09/2021	44.69	69
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]	10/2009	12,320.00 -	17,079.00	11,737.00	12/2016 -	03/2023	38.63	75
	Total		27,271.00 -	40,499.00	32,228.38				
	<u>CIVIL AVIATION</u>								
	<u>Airport Authority Of India Limited</u>								
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	314.61 -	441.33	85.79	09/2018 -	06/2020	40.28	21
	Total		314.61 -	441.33	85.79				
	<u>COAL</u>								
	<u>Eastern Coal Fields Limited</u>								
5	RANIGANJ MASTER PLAN - [N06000163]	08/2009	2,661.73 -	5,146.48	364.72	08/2019 -	08/2024	93.35	60
	<u>Neyveli Lignite Corporation</u>								
6	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	06/2011	5,907.11 -	7,080.41	6,954.15	12/2015 -	03/2020	19.86	51
	<u>Singareni Colliers Company Limited</u>								
7	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	12.27	03/2015 -	03/2021	114.60	72
8	KAKATIAKHANI OPENCAST-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	99.56	03/2019 -	03/2020	11.42	12
9	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	326.69	03/2012 -	03/2024	80.24	144
10	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 -	473.22	18.60	03/2015 -	03/2021	5.85	72
11	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	416.88	03/2012 -	03/2023	16.86	132
	<u>South-Eastern Coal Fields Limited</u>								
12	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	195.34	03/2015 -	03/2020	201.44	60

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(January 2020)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	<u>Western Coal Fields Limited</u>								
13	KAMPTEE DEEP OC MINE - [N06000141	11/2015	277.65 -	313.34	118.18	03/2021 -	03/2024	12.85	36
14	ADASA UG TO OC - [N06000133	08/2015	288.90 -	333.43	38.82	03/2023 -	03/2024	15.41	12
	Total		10,962.73 -	15,536.55	8,545.21				
	<u>COMMERCE AND INDUSTRY</u>								
	<u>India International Convention And Expo Centre</u>								
15	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002	11/2017	4,773.00 -	5,178.00	1,309.65	12/2019 -	09/2020	8.49	9
	Total		4,773.00 -	5,178.00	1,309.65				
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Hospital Services Consultancy Corporation Ltd</u>								
16	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012	07/2016	152.95 -	177.92	147.31	02/2018 -	03/2020	16.33	25
17	AIIMS - MOTHER AND CHILD BLOCK - [N21000008	12/2013	204.44 -	270.00	210.75	05/2017 -	06/2020	32.07	37
18	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017	08/2017	272.19 -	272.54	204.08	03/2019 -	03/2020	.13	12
19	AIIMS - OPD(NEW) - [N21000009	08/2014	293.65 -	325.00	304.62	05/2017 -	01/2020	10.68	32
20	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003	02/2013	414.11 -	499.23	337.32	11/2013 -	09/2020	20.55	82
	Total		1,337.34 -	1,544.69	1,204.08				
	<u>HUMAN RESOURCE DEVELOPMENT</u>								
	<u>Rail India Technical And Economic Service</u>								
21	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001	09/2013	484.32 -	626.26	-	09/2014 -	12/2020	29.31	75
	Total		484.32 -	626.26	.00				
	<u>PETROLEUM</u>								
	<u>Bharat Petroleum Corporation Limited</u>								
22	HALDIA LPG IMPORT FACILITY - [N16000223	03/2015	694.00 -	1,097.54	856.34	10/2018 -	02/2020	58.15	16

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(January 2020)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
23	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]	12/2015	1,112.00 -	1,507.24	566.00	06/2019 -	02/2022	35.54	32
24	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT (PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29 -	5,245.96	4,137.20	08/2018 -	02/2020	14.33	18
	<u>Gas Authority Of India Limited</u>								
25	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]	06/2009	2,915.00 2,915.00	4,915.00	2,784.58	12/2012 -	02/2022	68.61	110
	<u>Hindustan Petroleum Corporation Limited</u>								
26	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	07/2016	20,928.00 -	26,264.00	8,584.07	07/2020 -	07/2022	25.50	24
	<u>Indian Oil Corporation Limited</u>								
27	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	05/2016	4,497.00 -	6,025.00	1,588.02	12/2018 -	02/2021	33.98	26
	<u>Mangalore Refinery And Petrochemicals Limited</u>								
28	SEA WATER DESALINATION PLANT - [N16000319]	11/2017	581.00 -	621.00	154.66	03/2020 -	11/2020	6.88	8
	<u>Oil & Natural Gas Corporation Limited</u>								
29	DEVELOPMENT OF B-147 FIELD - [N16000292]	02/2017	546.15 -	565.15	468.71	11/2019 -	03/2020	3.48	4
30	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT (MOPS) - [N16000128]	03/2011	861.79 -	1,683.06	1,386.15	05/2013 -	02/2020	95.30	81
31	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	1,933.09	03/2015 -	03/2020	29.42	60
32	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	2,369.08	04/2018 -	05/2020	1.77	25
33	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]	02/2019	3,660.71 -	3,740.05	373.79	04/2021 -	05/2021	2.17	1
34	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]	02/2017	4,006.83 -	4,475.92	2,975.26	05/2021 -	12/2021	11.71	7
	<u>Oil India Limited</u>								
35	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	438.84	268.45	03/2017 -	06/2020	24.47	39
36	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	01/2018	543.91 -	682.90	71.46	02/2020 -	06/2020	25.55	4
	Total		50,537.56 -	63,174.50	28,516.86				
	<u>POWER</u>								
	<u>National Hydro-Electric Power Corporation</u>								

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(January 2020)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
37	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	9,997.11	7,761.19	09/2009 -	12/2021	155.06	147
38	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	19,496.34	11,842.12	09/2010 -	08/2023	210.19	155
	<u>National Thermal Power Corporation</u>								
39	RAMMAM-III HEPP (3X40 MW) - [N18000178]	09/2014	1,381.84 -	1,592.34	526.08	09/2019 -	11/2022	15.23	38
40	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	5,867.38	4,346.71	03/2013 -	12/2021	96.99	105
41	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	9,583.00	8,056.25	07/2012 -	09/2020	79.02	98
42	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	09/2014	9,188.98 -	10,016.10	7,036.74	07/2019 -	09/2020	9.00	14
43	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	03/2015	9,870.51 -	11,148.86	9,430.15	01/2020 -	02/2020	12.95	1
44	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]	04/2012	9,750.89 -	12,176.28	10,103.00	02/2017 -	06/2020	24.87	40
45	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	12,826.56	10/2017 -	03/2020	7.55	29
46	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	12,865.92	12,503.29	01/2018 -	03/2020	10.55	26
47	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 -	13,740.53	10,182.96	12/2018 -	08/2020	9.64	20
48	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,164.05	9,965.78	06/2019 -	03/2022	5.55	33
49	NPCCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	17,304.00	14,367.00	05/2018 -	06/2021	33.47	37
50	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	21,312.11	16,928.07	10/2011 -	08/2021	145.16	118
	<u>North East Electric Power Corporation</u>								
51	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	7,927.34	7,743.76	12/2009 06/2016	06/2020	217.49	126
	<u>Power Grid Corporation Of India Limited</u>								
52	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03	200.16	07/2017 -	01/2020	27.92	30
53	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	546.36	470.71	11/2016 -	03/2020	4.61	40
54	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	590.30	06/2014 -	02/2020	31.17	68
55	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	1,283.60	04/2016 -	02/2020	38.61	46
56	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]	10/2008	4,824.12 -	5,071.94	4,595.36	10/2012 -	03/2020	5.14	89

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(January 2020)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
57	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,880.36	1,886.30	12/2018 -	12/2020	34.61	24
58	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,072.36	1,402.48	12/2018 -	12/2020	90.82	24
59	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	14,719.10	12,824.45	08/2013 -	03/2022	32.24	103
	<u>Thdc India Limited</u>								
60	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	4,397.80	1,858.35	06/2013 -	12/2022	76.51	114
	Total		1,54,155.88 -	2,24,410.00	168,731.37				
	<u>RAILWAYS</u>								
	<u>Central Railways</u>								
61	3RD LINE BETWEEN BHUSAVAL-JALGAON - [N22000247]	04/2011	184.06 -	312.00	293.06	03/2019 -	03/2020	69.51	12
62	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89 -	1,377.48	318.59	03/2021 -	03/2022	73.73	12
63	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181]	02/1997	2,271.50 -	4,517.49	2,495.07	03/2021 -	03/2022	98.88	12
	<u>Container Corporation Of India</u>								
64	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 -	235.00	10.88	03/2019 -	12/2020	.21	21
	<u>East Central Railways</u>								
65	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	477.88 283.95	751.55	674.58	03/2012 -	03/2020	57.27	96
66	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]	04/2009	548.00 -	819.01	525.18	03/2020 -	03/2022	49.45	24
67	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	324.73 -	1,050.00	1,041.96	03/2012 -	03/2020	223.35	96
68	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 -	1,185.73	60.65	03/2021 -	03/2022	62.06	12
69	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 -	1,215.54	156.95	03/2021 -	03/2022	63.37	12
	<u>East Coast Railway</u>								
70	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 -	238.03	205.65	03/2020 -	03/2021	52.77	12
71	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	04/2015	701.61 -	810.02	139.27	11/2018 -	03/2022	15.45	40

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(January 2020)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
72	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,160.83	749.76	03/2020 -	03/2023	.07	36
73	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	1,111.99 -	1,539.28	972.93	02/2019 -	03/2022	38.43	37
74	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07	780.24	06/2021 -	06/2024	137.80	36
75	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]	04/2015	2,499.71 -	3,382.95	447.56	03/2022 -	03/2024	35.33	24
76	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	2,923.13 -	3,791.66	1,270.24	03/2009 -	06/2024	29.71	183
	<u>Eastern Railways</u>								
77	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	12.02	108
78	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]	04/2010	494.54 -	494.59	32.00	03/2005 -	03/2025	.01	240
79	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]	04/1987	406.99 -	545.70	148.49	03/2006 -	03/2025	34.08	228
80	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	499.96 -	680.68	159.70	02/2012 -	03/2025	36.15	157
81	HANSDIHA-GODDA NL - [N22000236]	04/2011	542.18 -	693.80	474.79	03/2020 -	03/2021	27.96	12
82	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]	04/2005	595.51 -	769.40	103.08	03/2017 -	03/2025	29.20	96
83	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]	04/2001	923.52 -	995.10	507.56	03/2016 -	03/2025	7.75	108
84	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 -	1,425.44	637.56	02/2013 -	03/2024	134.80	133
85	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,619.48	872.43	03/2019 12/2009	03/2025	36.22	72
86	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	2,137.81	300.18	03/2022 -	03/2025	133.39	36
	<u>Indian Railway Construction Company Limited</u>								
87	GEVRA ROAD PENDRA ROAD - [N22000488]	02/2014	2,288.00 -	4,970.11	635.13	03/2022 -	12/2022	117.23	9
	<u>Metropolitan Rapid Transport Projects</u>								
88	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	2,980.41	1,457.78	03/2004 -	03/2021	501.57	204
89	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	75.91	63
	<u>North Central Railway</u>								

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(January 2020)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
90	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96 -	3,845.60	148.26	03/2022 -	12/2024	32.02	33
	<u>North East Frontier Railway</u>								
91	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]	04/1983	297.32 -	614.00	275.07	03/2019 -	03/2020	106.51	12
92	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 -	670.00	82.81	03/2020 -	09/2021	17.62	18
93	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	314.00 -	728.00	731.27	03/2019 -	03/2020	131.85	12
94	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR [N22000086]	09/2006	385.20 -	1,532.00	652.15	03/2019 -	03/2020	297.72	12
95	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	532.87 -	2,145.00	935.62	03/2019 -	03/2020	302.54	12
96	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	1,180.19 -	4,541.00	3,346.08	12/2008 -	03/2021	284.77	147
97	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 -	5,021.45	3,183.01	03/2014 -	03/2022	109.80	96
98	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	2,326.52 -	5,806.81	876.09	03/2015 -	10/2021	149.59	79
99	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 -	12,524.00	9,599.02	03/2011 -	03/2022	181.17	132
	<u>North Eastern Railway</u>								
100	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	9.63	04/2016 -	06/2020	.16	50
101	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	370.93	01/2019 -	01/2020	61.80	12
	<u>North Western Railway</u>								
102	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	303.56	285.01	11/2019 -	12/2020	42.26	13
103	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	348.55	248.71	12/2019 -	02/2021	41.64	14
104	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	410.00	381.92	02/2019 -	02/2020	69.36	12
105	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	685.99	99.38	03/2020 -	04/2022	14.33	25
106	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	886.41	568.73	02/2019 -	06/2021	116.16	28
	<u>Northern Railway</u>								
107	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	750.00	290.62	12/2011 -	03/2021	161.32	111
108	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 -	859.00	835.35	03/2016 -	03/2021	37.44	60

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(January 2020)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
109	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	450.00 -	2,200.00	668.77	07/2012 -	03/2024	388.89	140
110	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	27,949.00	20,501.11	11/2002 -	06/2022	1,017.96	235
	<u>Rail Vikas Nigam Ltd.</u>								
111	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	396.00	388.21	03/2009 03/2009	06/2020	196.83	135
112	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD [N22000213	04/2012	632.68 -	816.55	720.70	03/2016 -	12/2020	29.06	57
113	BANASPANI- JAKHPURA - DOUBLING - [N22000412	03/2009	942.95 -	1,120.00	1,046.08	03/2019 -	06/2022	18.78	39
114	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404	04/2011	927.01 -	1,200.00	1,209.55	03/2019 -	03/2020	29.45	12
115	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410	03/2006	948.04 -	1,500.00	1,451.81	03/2020 -	03/2021	58.22	12
116	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	1,185.64 -	1,844.47	1,883.44	12/2017 -	03/2020	55.57	27
117	VIJAYWADA-GUDUGOLANU-BHIMAVARAM- NARSAPUR DL (221 KM) - [N22000313	03/2012	1,503.71 -	2,200.00	1,966.03	03/2020 -	03/2022	46.30	24
118	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407	03/2009	713.48 -	2,300.00	2,131.56	03/2020 -	03/2021	222.36	12
119	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109	04/2010	2,298.42 -	2,733.86	40.13	03/2014 -	12/2025	18.95	141
120	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297	04/2010	2,127.00 -	2,900.00	1,815.11	03/2023 -	03/2024	36.34	12
121	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111	04/2010	2,913.51 -	4,639.00	871.04	03/2016 -	03/2025	59.22	108
122	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110	04/2010	3,951.98 -	4,724.30	2,307.00	03/2016 -	03/2025	19.54	108
	<u>South Central Railway</u>								
123	MANMAD-PARBHANI-NANDED-SECUNDERABAD- GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432	04/2017	119.73 185.00	449.39	298.13	03/2022 -	12/2022	275.34	9
124	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261	04/2012	1,856.95 -	1,952.68	329.00	03/2023 -	03/2024	5.16	12
125	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	1,045.20 -	2,120.16	561.18	03/2009 -	03/2023	102.85	168
126	NADIKUDE-SRI KALAHASTI - [N22000286	04/2011	2,288.70 -	2,643.25	860.07	03/2021 -	03/2024	15.49	36
127	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205	04/1997	1,723.00 1.00	3,472.59	970.69	03/2000 -	03/2021	101.54	252

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(January 2020)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	<u>South East Central Railway</u>								
128	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00 -	852.50	39.69	12/2021 -	03/2023	272.27	15
129	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]	04/2008	872.00 -	1,226.51	1,066.54	12/2019 -	03/2020	40.65	3
130	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438]	04/2010	585.93 -	1,268.32	687.95	02/2019 -	12/2020	116.46	22
131	ANUPPUR-KATNI - [N22000485]	04/2015	1,370.00 -	1,370.94	332.76	12/2021 -	03/2023	.07	15
132	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	511.86 -	1,756.00	1,679.29	04/2020 -	01/2021	243.06	9
133	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	04/2015	1,973.00 -	1,973.64	185.98	03/2021 -	03/2023	.03	24
	<u>South Eastern Railway</u>								
134	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	358.68	278.34	12/2018 -	08/2020	38.92	20
135	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND [N22000323]	04/2012	148.77 -	377.00	183.96	12/2016 -	03/2020	153.41	39
136	DIGHA-JALESWAR INCLUDING MM FOR DIGHA- EGRA - [N22000160]	04/2010	651.00 -	1,009.00	7.96	03/2015 -	03/2025	54.99	120
137	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	1,312.96	610.19	03/2020 -	03/2021	35.38	12
138	BONDAMUNDA RANCHI DOUBLING - [N22000396]	03/2016	1,724.20 -	1,993.24	469.79	03/2021 -	12/2021	15.60	9
139	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL [N22000402]	04/1998	1,027.40 -	2,373.00	485.04	03/2003 -	03/2030	130.97	324
	<u>South Western Railway</u>								
140	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78 -	890.00	461.80	03/2017 -	03/2020	38.03	36
141	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 -	1,870.41	1,056.97	03/2019 -	03/2021	15.84	24
	<u>Southern Railway</u>								
142	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]	10/2013	187.26 -	231.67	167.12	04/2014 -	03/2020	23.72	71
143	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	303.98 -	980.00	683.11	03/2020 -	03/2021	222.39	12
144	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING [N22000451]	02/2015	760.00 -	1,182.31	446.00	03/2020 -	06/2021	55.57	15
145	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI [N22000079]	09/2007	724.69 -	2,072.50	1,471.60	02/2019 -	02/2020	185.98	12
	<u>West Central Railway</u>								

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(January 2020)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
146	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13 -	1,247.64	228.36	03/2022 -	09/2022	114.32	6
147	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60 -	2,909.99	1,975.34	03/2021 -	03/2023	585.35	24
148	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	8,248.50	1,986.78	05/2008 -	03/2023	3,230.57	178
	<u>Western Railway</u>								
149	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	125.76	03/2012 -	03/2022	1.06	120
150	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]	02/1991	551.51 -	809.07	635.52	03/2019 -	03/2020	46.70	12
151	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	858.96	534.00	03/2019 -	03/2022	167.87	36
152	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	04/2008	829.74 -	1,310.23	1,532.69	03/2020 -	03/2021	57.91	12
153	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	3,503.69 -	3,975.22	1,801.98	03/2022 -	03/2023	13.46	12
	Total		97,898.67 -	2,02,840.94	103,438.90				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>								
154	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]	03/2016	160.27 -	213.97	20.11	08/2019 -	08/2021	33.51	24
155	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]	03/2018	217.22 -	226.88	86.83	08/2018 -	06/2020	4.45	22
156	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]	06/2016	236.78 -	263.26	59.92	08/2019 -	08/2021	11.18	24
157	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]	08/2010	186.96 -	305.61	279.13	09/2014 -	06/2020	63.46	69
158	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]	08/2010	193.69 -	327.92	258.71	10/2010 -	06/2021	69.30	128
159	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DSIGN CH0.0) TO KM 275/622(DSIGN CH 5.12 - [N24000928]	10/2015	333.21 -	355.89	294.81	12/2015 -	01/2020	6.81	49
160	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]	08/2010	195.04 -	377.99	312.41	10/2010 -	-	93.80	116

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(January 2020)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
161	BALANCE WORK FOR REHABILITATION AND UPGRADE OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]	11/2017	392.33 -	428.55	253.99	03/2018 -	09/2020	9.23	30
162	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]	11/2013	497.05 -	881.05	624.54	05/2017 -	05/2020	77.26	36
163	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]	11/2010	624.41 -	992.67	886.01	03/2011 -	12/2020	58.98	117
164	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]	11/2011	954.43 -	1,191.51	235.61	09/2015 -	10/2021	24.84	73
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
165	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]	12/2016	138.93 155.00	155.00	79.91	01/2017 -	01/2020	11.57	36
166	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]	03/2016	373.07 -	387.00	216.07	08/2016 -	03/2020	3.73	43
	<u>National Highways Authority Of India</u>								
167	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 -	230.00	340.21	04/2008 -	03/2020	10.58	143
168	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]	05/2011	511.54 -	591.00	571.86	11/2013 -	03/2020	15.53	76
169	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]	10/2015	593.26 -	636.24	490.35	05/2018 -	06/2020	7.24	25
170	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]	11/2012	605.84 -	722.46	722.46	07/2018 -	02/2020	19.25	19
171	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]	10/2015	531.13 -	727.00	524.15	05/2018 -	09/2020	36.88	28
172	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]	10/2015	447.29 -	746.43	614.07	12/2017 -	06/2020	66.88	30
173	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	03/2017	754.54 -	756.27	193.96	03/2020 -	08/2021	.23	17
174	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	03/2017	988.34 -	1,043.28	1,035.00	03/2020 -	08/2020	5.56	5
175	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	03/2017	1,030.44 -	1,065.51	1,015.76	03/2020 -	05/2020	3.40	2
176	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]	03/2017	1,059.73 -	1,071.00	610.87	03/2017 -	11/2020	1.06	44

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(January 2020)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
177	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622	09/2016	950.69 -	1,108.00	1,399.33	08/2019 -	12/2020	16.55	16
178	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	03/2017	1,098.06 -	1,160.64	1,068.76	03/2020 -	08/2020	5.70	5
179	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 -	1,177.00	702.31	03/2020 -	07/2020	41.54	4
180	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 -	1,187.10	829.16	03/2020 -	05/2020	13.97	2
181	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704	09/2017	1,124.11 -	1,232.76	314.14	09/2017 -	05/2021	9.67	44
182	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.71 -	1,310.00	563.15	03/2020 -	08/2020	10.58	5
183	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 -	1,420.00	532.31	03/2020 -	03/2021	10.24	12
184	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	765.31	03/2020 -	06/2020	44.39	3
185	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693	06/2017	1,958.88 -	1,993.81	1,116.85	06/2020 -	02/2021	1.78	8
186	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 -	2,447.00	2,029.34	03/2020 -	06/2020	18.50	3
187	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807	03/2018	1,532.62 -	2,499.00	730.93	03/2021 -	04/2021	63.05	1
188	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600	08/2016	1,388.34 -	2,587.50	1,449.00	09/2019 -	03/2020	86.37	6
189	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224	10/2012	1,928.22 -	2,945.00	2,467.00	04/2015 -	06/2020	52.73	62
190	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,967.50	3,990.72	11/2011 -	03/2020	167.82	100
	Total		29,726.55 -	39,165.80	27,685.05				
	<u>STEEL</u>								
	<u>National Mineral Development Corporation (Nmdc)</u>								
191	NMDC INTEGRATED STEEL PLANT - [N12000086	01/2010	15,525.00 -	23,140.00	16,468.33	05/2015 -	07/2020	49.05	62
	Total		15,525.00 -	23,140.00	16,468.33				

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(January 2020)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	<u>TELECOMMUNICATIONS</u>								
	<u>Bharat Sanchar Nigam Limited</u>								
192	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]	01/2018	231.80 -	240.10	119.92	10/2018 -	02/2020	3.58	16
	<u>Department Of Telecommunication</u>								
193	NETWORK FOR SPECTRUM - [N26000101]	03/2012	13,334.00 -	24,664.00	12,146.00	07/2015 -	05/2020	84.97	58
	Total		13,565.80 -	24,904.10	12,265.92				
	<u>URBAN DEVELOPMENT</u>								
	<u>Central Public Works Department</u>								
194	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]	08/2016	294.00 -	350.69	219.60	04/2019 -	05/2020	19.28	13
195	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]	02/2014	388.00 -	490.00	442.51	05/2017 -	03/2020	26.29	34
196	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	118.00	06/2017 -	03/2021	.57	45
197	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]	12/2016	549.31 -	559.47	373.45	07/2019 -	08/2020	1.85	13
198	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	2,000.00	436.20	10/2019 -	03/2021	64.04	17
	<u>Kochi Metro Rail Corporation Ltd</u>								
199	KOCHI METRO RAIL PROJECT - [N28000081]	07/2012	5,181.79 -	6,218.14	5,817.11	07/2017 -	03/2020	20.00	32
	<u>National Building Construcion Corporation Ltd</u>								
200	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	06/2012	4,264.00 -	4,720.73	4,553.13	11/2019 -	05/2020	10.71	6
	Total		12,392.49 -	14,838.02	11,960.00				
	<u>WATER RESOURCES</u>								
	<u>Polavaram Project Authority</u>								
201	POLAVARAM IRRIGATION PROJECT - [N30000002]	02/2009	10,151.04 -	55,548.87	32,535.80	03/2020 -	12/2021	447.22	21
	Total		10,151.04 -	55,548.87	32,535.80				
	Grand Total		4,29,095.99	7,11,848.06	444,975.34				

Details of Projects Without Date of Commissioning

Annexure - VIII

Costing Rs. 150 Crore and above				(January 2020)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>CIVIL AVIATION</u>				
	<u>Airport Authority Of India Limited</u>				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI, TRIPURA	09/2015	338.93 -	06/2019 -	-
	Total		338.93 -		
	<u>COAL</u>				
	<u>Bharat Coking Coal Limited</u>				
2	MURADIH UG TURN-KEY PROJECT - [N06000096]BCCL, JHARKHAND	02/2011	339.88 -	04/2014 -	-
3	KAPURIA UG(PSLW) - [N06000108]BCCL, JHARKHAND	08/2011	988.35 -	04/2017 -	-
	<u>Neyveli Lignite Corporation</u>				
4	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC, RAJASTHAN	03/2015	522.45 -	09/2019 -	-
5	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC, TAMIL NADU	04/2013	1,458.17 709.06	06/2015 -	-
6	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC, RAJASTHAN	03/2015	513.63 -	12/2019 -	-
	<u>Singareni Colliers Company Limited</u>				
7	KAKATIYA LONGWALL - [N06000048]SCCL, TELANGANA	12/2008	453.63 -	12/2012 -	-
8	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL, TELANGANA	03/2010	181.19 -	03/2012 -	-
	<u>Western Coal Fields Limited</u>				
9	NEW MAJRI UG TO OC - [N06000128]WCL, MAHARASHTRA	05/2015	295.56 -	03/2019 -	-
10	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL, MAHARASHTRA	02/2016	198.68 -	03/2019 -	-
11	BHATADI EXPANSION OC MINE - [N06000150]WCL, MAHARASHTRA	02/2016	304.52 -	03/2019 -	-
12	GAURI DEEP OC - [N06000181]WCL, MAHARASHTRA	10/2016	164.96 -	03/2019 -	-
	Total		5,421.02 -		
	<u>FERTILISERS</u>				
	<u>National Fertiliser Limited</u>				
13	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]NFL, HARYANA	01/2018	215.92 -	11/2019 -	11/2019

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (January 2020)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	Total		215.92		
	<u>PETROLEUM</u>				
	<u>Chennai Petroleum Corporation Limited</u>				
14	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU	03/2013	3,110.36	11/2015	-
	<u>Hindustan Petroleum Corporation Limited</u>				
15	REDEVELOPMENT/ EXPANSION OF MEERUT DEPOT FOR ENHANCING PRODUCT HANDLING CAPACITY - [N16000366]HPCL,UTTAR PRADESH	08/2016	154.84	11/2019	11/2019
	<u>Indian Oil Corporation Limited</u>				
16	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	10/2015	607.06	10/2017	-
17	120 TMTA LPG BOTTLING PLANT AT GORAKHPUR UP - [N16000354]IOCL,UTTAR PRADESH	03/2014	204.00	09/2019	-
	<u>Indian Strategic Petroleum Reserves Ltd</u>				
18	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KARNATAKA	01/2006	993.00	01/2012	-
	<u>Mangalore Refinery And Petrochemicals Limited</u>				
19	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]MANGALORE REFIN,KARNATAKA	05/2015	224.00 207.00	04/2019	-
20	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]MANGALORE REFIN,KARNATAKA	10/2015	135.00 171.00	03/2019	-
	<u>Oil India Limited</u>				
21	50MW WIND ENERGY POWER PROJECT - [N16000298]OIL,MULTI STATE	11/2015	500.00	06/2017	-
22	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM	07/2011	350.00	01/2019	-
23	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35	03/2015	-
	Total		7,149.61		
	<u>POWER</u>				
	<u>National Hydro-Electric Power Corporation</u>				
24	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR	12/1999	578.62	06/2006	-
	<u>National Thermal Power Corporation</u>				
25	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH	09/2015	3,004.00	11/2019	11/2019
26	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47	09/2016	-
27	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00	08/2017	-
28	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,238.00	10/2017	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (January 2020)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>Power Grid Corporation Of India Limited</u>				
29	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE	03/2017	283.72 -	11/2019 -	11/2019
	Total		17,552.77 -		
	<u>HEALTH AND FAMILY WELFARE</u>				
	<u>Hospital Services Consultancy Corporation Ltd</u>				
30	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC, WEST BENGAL	08/2016	244.00 -	09/2018 -	05/2019
31	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC, WEST BENGAL	12/2014	168.90 -	05/2017 -	07/2019
32	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC, HARYANA	09/2014	505.58 -	03/2018 -	09/2019
	Total		918.48 -		
	<u>RAILWAYS</u>				
	<u>Central Railways</u>				
33	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]CR, MAHARASHTRA	02/2016	2,750.00 -	03/2024 -	-
	<u>Container Corporation Of India</u>				
34	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI, MAHARASHTRA	10/2013	305.00 -	03/2019 -	12/2019
35	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI, ANDHRA PRADESH	01/2013	387.70 -	03/2018 -	-
36	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI, CHHATISGARH	05/2014	207.00 -	03/2018 -	-
37	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI, GUJARAT	10/2013	343.00 -	03/2019 -	-
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>				
38	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC, MULTI STATE	10/2006	11,589.00 30,357.00	- -	-
	<u>East Central Railways</u>				
39	RAJGIR HISUA TALAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR, BIHAR	04/1998	180.82 726.31	- -	10/2019
40	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR, BIHAR	04/2001	406.92 -	- -	-
41	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR, BIHAR	01/1991	332.15 546.71	07/2014 -	-
42	ARA-BHABHUA ROAD (NL) - [N22000166]ECR, BIHAR	04/2008	633.87 -	- -	-
43	NAWADA-LAXMIPUR (NL) - [N22000167]ECR, BIHAR	04/2008	620.57 -	- -	-
44	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR, BIHAR	04/2008	445.25 -	- -	-
45	GAYA-CHATRA (NL) - [N22000169]ECR, MULTI STATE	04/2008	415.67 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(January 2020)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
46	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-
47	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-
48	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-
49	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-
50	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
	<u>Eastern Railways</u>				
51	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	05/2019
	<u>Kolkata Metro Rail Corporation Limited</u>				
52	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-
	<u>Metropolitan Rapid Transport Projects</u>				
53	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-
54	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP, TAMIL NADU	04/2006	495.74 -	06/2013 -	-
55	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N220000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	-
	<u>North Central Railway</u>				
56	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-
57	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR, MULTI STATE	04/2010	2,030.50 -	- -	-
	<u>North East Frontier Railway</u>				
58	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	12/2015 -	-
59	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 -	03/2019 -	-
60	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE	04/1999	819.23 -	- -	-
61	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHOWA-JAIN - [N22000499]NFR, WEST BENGAL	02/1999	380.60 -	04/2010 -	-
	<u>North Eastern Railway</u>				
62	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH	03/2015	1,295.42 -	03/2022 -	12/2019
63	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-
64	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(January 2020)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
65	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
66	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-
67	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-
68	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH	04/2016	602.50 -	- -	-
	<u>North Western Railway</u>				
69	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	10/2018 -	12/2019
70	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-
71	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
72	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
73	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-
	<u>Rail India Technical And Economic Service</u>				
74	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-
	<u>Railway Electrification</u>				
75	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-
	<u>South Central Railway</u>				
76	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	164.36 -	02/2009 -	-
77	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	458.25 458.25	- -	-
78	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 2,911.84	- -	-
79	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 2,184.83	- -	-
80	GUDUR-DURGARAJPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	761.37 761.37	- -	-
81	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 829.00	- -	-
82	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 3,873.07	- -	-
	<u>South Eastern Railway</u>				
83	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-
84	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-
	<u>Southern Railway</u>				
85	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	03/2019 -	12/2019
86	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	1,566.00 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(January 2020)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
87	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	227.40 -	- -	-
88	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	- -	-
89	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	151.84 -	02/2019 -	-
90	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-
91	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
92	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-
93	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-
94	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
95	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
96	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-
97	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 -	- -	-
98	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	- -	-
99	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	03/2005 -	-
100	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-
101	ATTIPATTU - KORUKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU	02/1999	257.00 257.00	03/2018 -	-
	<u>Western Railway</u>				
102	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	03/2017
103	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT	03/2017	243.60 -	- -	-
104	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-
105	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-
106	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-
107	PALANPUR KHOBIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 -	- -	-
	Total		59,883.63 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(January 2020)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>				
108	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	12/2019
109	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA	03/2018	256.15 -	12/2019 -	12/2019
110	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]MoRTH,ANDHRA PRADESH	01/2016	386.09 -	05/2016 12/2019	05/2018
111	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929]MoRTH,ANDHRA PRADESH	09/2016	372.68 -	02/2017 12/2019	02/2019
112	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O - [N24000871]MoRTH,WEST BENGAL	08/2014	600.87 720.97	11/2017 05/2019	05/2019
113	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873]MoRTH,WEST BENGAL	08/2014	823.20 937.76	11/2017 06/2019	06/2019
114	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]MoRTH,WEST BENGAL	04/2014	279.70 398.52	08/2017 07/2019	07/2019
115	AJANTHA TO BULDHANA - [N24001008]MoRTH,A & N ISLANDS	02/2017	401.00 401.00	07/2019 -	07/2019
116	MANTHA TALUKAS BORDER TO PARTUR - [N24001033]MoRTH,MAHARASHTRA	01/2017	486.19 486.19	07/2019 -	07/2019
117	PARTUR TO MAJALGAON - [N24001034]MoRTH,MAHARASHTRA	01/2017	420.57 420.57	07/2019 -	07/2019
118	MAJALGAON TO KAIJ - [N24001036]MoRTH,MAHARASHTRA	01/2017	413.99 -	07/2019 -	07/2019
119	KAIJ TO KUSALAM - [N24001037]MoRTH,MAHARASHTRA	01/2017	554.78 554.78	07/2019 -	07/2019
120	SHIROD SHAHPURER TO NANDED - [N24001041]MoRTH,MAHARASHTRA	01/2017	211.34 211.34	07/2019 -	07/2019
121	MUL TO CHANDRAPUR - [N24001117]MoRTH,MAHARASHTRA	12/2016	162.34 -	07/2019 -	07/2019
122	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2 - - [N24001147]MoRTH,UTTAR PRADESH	10/2016	239.63 -	02/2019 -	07/2019
123	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 - [N24000962]MoRTH,MADHYA PRADESH	09/2016	178.23 -	09/2018 -	08/2019
124	KATOL TO WARUD - [N24001019]MoRTH,MAHARASHTRA	01/2017	463.62 664.00	06/2019 -	08/2019
125	AMD I TO SAONER - [N24001021]MoRTH,MAHARASHTRA	01/2017	396.91 396.91	06/2019 -	08/2019
126	AHMADPUR TO PIMPLA - [N24001029]MoRTH,MAHARASHTRA	01/2017	422.38 422.38	08/2019 -	08/2019
127	PIMPLA TO MANJARUMBHA - [N24001030]MoRTH,MAHARASHTRA	01/2017	595.77 595.77	08/2019 -	08/2019
128	MANJUSUMBA TO CHUMBALI - [N24001031]MoRTH,MAHARASHTRA	01/2017	228.54 228.54	08/2019 -	08/2019
129	AHMEDNAGAR TO BARAMATI - [N24001100]MoRTH,MAHARASHTRA	01/2017	955.40 -	08/2019 -	08/2019

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(January 2020)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
130	NANDED TO JALKOT - [N24001069]MoRTH,MAHARASHTRA	12/2017	456.93 457.00	09/2019 -	09/2019
131	NASRATPUR TO BARASGAON - [N24001112]MoRTH,MAHARASHTRA	07/2016	406.54 406.54	09/2019 -	09/2019
132	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO - [N24001143]MoRTH,UTTAR PRADESH	10/2016	176.94 177.00	10/2018 -	09/2019
133	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH	01/2012	410.72 -	04/2015 -	10/2019
134	CHIKALI TO KHAMGAON - [N24001012]MoRTH,MAHARASHTRA	02/2017	548.03 548.00	06/2019 -	10/2019
135	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]MoRTH,UTTAR PRADESH	11/2016	215.16 215.00	09/2019 -	10/2019
136	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]MoRTH,UTTAR PRADESH	10/2013	445.89 653.00	03/2017 -	10/2019
137	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]MoRTH,WEST BENGAL	03/2016	271.17 291.20	11/2018 11/2019	11/2019
138	JAHIRABAD TO LATUR - [N24001040]MoRTH,MAHARASHTRA	01/2017	461.96 461.96	11/2019 -	11/2019
139	JALGAON TO BHADGAON - [N24001045]MoRTH,MAHARASHTRA	01/2018	307.54 308.00	11/2019 -	11/2019
140	BHADGAON TO CHALISGAON - [N24001047]MoRTH,MAHARASHTRA	01/2018	259.55 260.00	11/2019 -	11/2019
141	TASGAON TO SHIRDHON - [N24001054]MoRTH,MAHARASHTRA	01/2017	195.64 196.00	11/2019 -	11/2019
142	MANGRUPHIR TO MAHAN - [N24001087]MoRTH,MAHARASHTRA	03/2018	222.13 222.13	11/2019 -	11/2019
143	SAKOLI TO BHANDARA - [N24001118]MoRTH,MAHARASHTRA	01/2017	362.96 362.96	06/2019 -	11/2019
144	NASHIK TO PETH - [N24001121]MoRTH,MAHARASHTRA	12/2015	289.60 -	11/2018 -	11/2019
145	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]MoRTH,ARUNACHAL PRADESH	03/2012	207.03 389.45	05/2012 05/2015	12/2019
146	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]MoRTH,SIKKIM	04/2013	151.59 240.58	08/2013 -	12/2019
147	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]MoRTH,SIKKIM	01/2013	182.28 -	02/2013 -	12/2019
148	KARASWADA TO BAMBOLIM - [N24001005]MoRTH,GOA	03/2017	852.67 852.67	12/2019 -	12/2019
149	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA	02/2017	203.21 203.00	05/2019 -	12/2019
150	SHEGAON TO DEORI PHATA - [N24001010]MoRTH,MAHARASHTRA	02/2017	373.10 373.00	05/2019 -	12/2019
151	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA	01/2017	385.87 386.00	06/2019 -	12/2019
152	NAGAJ TO VAJJAPUR - [N24001023]MoRTH,MAHARASHTRA	01/2017	376.72 377.00	06/2019 -	12/2019

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(January 2020)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
153	INDAPUR TO AGARDANDA - [N24001025]MoRTH,MAHARASHTRA	01/2017	355.17 -	07/2019 -	12/2019
154	SHAHNUR PATGAON SECTION I - [N24001027]MoRTH,MAHARASHTRA	01/2018	150.79 150.79	12/2019 -	12/2019
155	PATGAON KHOPOLI SECTION I - [N24001028]MoRTH,MAHARASHTRA	01/2018	170.00 -	12/2019 -	12/2019
156	MANSAR TO SALAIKHURD - [N24001035]MoRTH,MAHARASHTRA	01/2018	418.36 -	12/2019 -	12/2019
157	SALAIKHURD TO TIRORA - [N24001042]MoRTH,MAHARASHTRA	01/2018	415.25 415.25	12/2019 -	12/2019
158	KARAD TO VITA - [N24001049]MoRTH,MAHARASHTRA	01/2018	344.85 245.00	12/2019 -	12/2019
159	VITA TO NAGAJ - [N24001050]MoRTH,MAHARASHTRA	03/2018	304.58 305.00	12/2019 -	12/2019
160	NALDURG TO AKKALKOT - [N24001051]MoRTH,MAHARASHTRA	02/2018	274.50 275.00	12/2019 -	12/2019
161	SANGOLA TO JATH - [N24001052]MoRTH,MAHARASHTRA	01/2018	257.38 257.00	12/2019 -	12/2019
162	KARWANDI TO RAJURI - [N24001058]MoRTH,MAHARASHTRA	03/2018	276.95 277.00	12/2019 -	12/2019
163	SHIVUR TO YEOLA - [N24001059]MoRTH,MAHARASHTRA	03/2018	181.08 -	12/2019 -	12/2019
164	PALPHATA TO PHULAMBARI - [N24001060]MoRTH,MAHARASHTRA	03/2018	227.19 227.00	12/2019 -	12/2019
165	CHIKALI TO DHAD - [N24001061]MoRTH,MAHARASHTRA	03/2018	189.46 189.00	12/2019 -	12/2019
166	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]MoRTH,MAHARASHTRA	03/2018	336.21 336.00	12/2019 -	12/2019
167	PARBHANI TO GANGKHED - [N24001065]MoRTH,MAHARASHTRA	03/2018	238.19 238.00	12/2019 -	12/2019
168	LATUR TO PANGAON - [N24001066]MoRTH,MAHARASHTRA	03/2018	336.47 336.00	12/2019 -	12/2019
169	OMREGA TO AUSA - [N24001067]MoRTH,MAHARASHTRA	03/2018	272.04 272.00	12/2019 -	12/2019
170	WASHIM TO DASTAPUR - [N24001068]MoRTH,MAHARASHTRA	03/2018	165.51 -	12/2019 -	12/2019
171	DASTAPUR TO KARANJA - [N24001070]MoRTH,MAHARASHTRA	03/2018	182.63 -	12/2019 -	12/2019
172	KHERDA TO NAGZARI - [N24001072]MoRTH,MAHARASHTRA	03/2018	181.30 -	12/2019 -	12/2019
173	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA	03/2018	249.29 -	12/2019 -	12/2019
174	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA	03/2018	219.91 -	12/2019 -	12/2019
175	KUNDAL TO WAZAR - [N24001077]MoRTH,MAHARASHTRA	01/2018	225.25 225.00	12/2019 -	12/2019
176	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA	03/2018	228.31 -	12/2019 -	12/2019
177	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]MoRTH,MAHARASHTRA	03/2018	294.87 295.00	12/2019 -	12/2019

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(January 2020)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
178	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA	03/2018	223.46 -	12/2019 -	12/2019
179	CHIKLI TO TAKARKHED - [N24001083]MoRTH,MAHARASHTRA	03/2018	393.10 393.10	12/2019 -	12/2019
180	TAKARKHED TO JALNA - [N24001085]MoRTH,MAHARASHTRA	09/2017	417.90 418.00	06/2019 -	12/2019
181	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA	03/2018	177.84 177.00	12/2019 -	12/2019
182	MALEGAON TO RISOD - [N24001089]MoRTH,MAHARASHTRA	02/2018	303.24 303.24	12/2019 -	12/2019
183	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]MoRTH,MAHARASHTRA	03/2016	536.65 356.00	12/2019 -	12/2019
184	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA	12/2017	309.94 310.00	12/2019 -	12/2019
185	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA	12/2017	244.04 244.00	03/2019 -	12/2019
186	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA	01/2018	264.41 264.00	03/2019 -	12/2019
187	WARDHA TO HINGAGHAT - [N24001098]MoRTH,MAHARASHTRA	01/2018	216.90 216.90	12/2019 -	12/2019
188	PEN TO KHOPOLI - [N24001106]MoRTH,MAHARASHTRA	03/2018	301.39 302.00	03/2018 -	12/2019
189	CHALISGAON TO NANDGAON - [N24001108]MoRTH,MAHARASHTRA	03/2018	206.97 207.00	12/2019 -	12/2019
190	KUSUMBA TO MALEGAON - [N24001109]MoRTH,MAHARASHTRA	03/2018	243.45 244.00	12/2019 -	12/2019
191	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA	02/2018	355.99 355.99	12/2019 -	12/2019
192	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM - [N24001153]MoRTH,ASSAM	11/2010	197.37 -	02/2014 -	12/2019
193	REHABILITATION AND UPGRADATION OF BARAICH -SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA - [N24001202]MoRTH,UTTAR PRADESH	03/2016	388.83 -	12/2019 -	12/2019
194	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]MoRTH,TELANGANA	01/2014	270.00 -	03/2016 -	-
195	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA	03/2015	153.21 -	01/2017 -	-
196	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]MoRTH,GOA	03/2015	297.00 -	04/2018 -	-
197	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]MoRTH,MAHARASHTRA	03/2015	168.30 -	- -	-
198	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]MoRTH,MAHARASHTRA	08/2014	187.79 -	07/2016 -	-
199	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]MoRTH,MAHARASHTRA	01/2014	446.77 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(January 2020)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
200	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]MoRTH,GOA	03/2015	298.33 -	- -	-
201	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]MoRTH,GOA	03/2015	184.05 -	- -	-
202	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]MoRTH,GOA	03/2015	280.16 -	- -	-
203	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]MoRTH,KERALA	01/2014	255.75 348.00	09/2017 -	-
204	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]MoRTH,ANDHRA PRADESH	07/2015	333.21 333.21	12/2015 -	-
205	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MoRTH,MAHARASHTRA	10/2015	289.60 -	- -	-
206	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MoRTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-
207	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]MoRTH,CHHATISGARH	12/2015	291.05 -	- -	-
208	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]MoRTH,ANDHRA PRADESH	01/2014	195.45 -	11/2014 -	-
209	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]MoRTH,CHHATISGARH	11/2015	485.44 -	12/2015 -	-
210	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MoRTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-
211	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MoRTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-
212	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MoRTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-
213	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MoRTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-
214	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MoRTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-
215	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]MoRTH,ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	-
216	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]MoRTH,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-
217	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]MoRTH,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(January 2020)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
218	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]MoRTH,SIKKIM	04/2013	166.27 -	08/2013 -	-
219	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]MoRTH,NAGALAND	12/2010	1,296.00 -	02/2011 -	-
220	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MoRTH,TAMIL NADU	03/2015	258.97 -	08/2015 -	-
221	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MoRTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-
222	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I- - [N24000318]MoRTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-
223	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MoRTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-
224	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA	01/2015	225.81 -	- -	-
225	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MoRTH,RAJASTHAN	12/2015	621.43 -	06/2018 -	-
226	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-
227	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MoRTH,KARNATAKA	03/2015	159.12 -	11/2015 -	-
228	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]MoRTH,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	-
229	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE - [N24000373]MoRTH,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	-
230	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]MoRTH,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	-
231	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MoRTH,KARNATAKA	01/1991	219.40 -	01/2018 -	-
232	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MoRTH,ODISHA	01/1991	218.63 -	10/2017 -	-
233	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH,BIHAR	01/1991	675.00 -	- -	-
234	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]MoRTH,PUNJAB	12/2015	766.36 -	- 09/2019	-
235	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]MoRTH,PUNJAB	11/2015	847.02 -	- 12/2019	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(January 2020)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
236	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]MoRTH,ASSAM	11/2010	268.08 -	05/2017 -	-
237	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]MoRTH,MADHYA PRADESH	08/2015	257.80 -	- -	-
238	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]MoRTH,ASSAM	11/2010	470.20 -	02/2011 -	-
239	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MoRTH,WEST BENGAL	01/1991	322.00 -	03/2018 -	-
240	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MoRTH,BIHAR	01/1991	282.41 -	08/2016 -	-
241	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MoRTH,BIHAR	01/1991	358.22 -	10/2016 -	-
242	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]MoRTH,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-
243	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]MoRTH,ASSAM	11/2014	218.31 -	02/2018 -	-
244	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MoRTH,ODISHA	01/1991	229.41 -	05/2018 -	-
245	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]MoRTH,ODISHA	07/2014	342.05 -	01/2017 -	-
246	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH,GOA	10/2015	936.40 -	- -	-
247	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]MoRTH,RAJASTHAN	09/2012	511.00 -	10/2013 -	-
248	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]MoRTH,RAJASTHAN	09/2012	511.00 -	10/2013 -	-
249	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH,GOA	12/2015	773.98 -	- -	-
250	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MoRTH,GOA	12/2015	819.95 -	- -	-
251	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MoRTH,BIHAR	01/1991	478.35 -	- -	-
252	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]MoRTH,ODISHA	12/2011	159.39 -	11/2017 -	-
253	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]MoRTH,PUNJAB	06/2015	892.17 -	- 02/2018	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(January 2020)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
254	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH,ODISHA	12/2011	191.08 -	08/2015 -	-
255	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIK 40 - [N24000530]MoRTH,BIHAR	01/1991	154.62 -	- -	-
256	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]MoRTH,BIHAR	01/1991	319.68 -	- -	-
257	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MoRTH,BIHAR	10/2013	278.39 -	08/2014 -	-
258	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MoRTH,BIHAR	11/2013	683.83 -	07/2016 -	-
259	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MoRTH,BIHAR	02/2014	665.50 -	07/2016 -	-
260	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MoRTH,BIHAR	02/2016	178.85 -	05/2016 -	-
261	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MoRTH,BIHAR	02/2016	369.77 -	06/2016 -	-
262	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MoRTH,BIHAR	02/2016	553.30 -	05/2016 -	-
263	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-
264	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPR - [N24000580]MoRTH,BIHAR	03/2015	206.80 -	07/2016 -	-
265	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MoRTH,BIHAR	08/2015	288.24 -	11/2015 -	-
266	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH,MAHARASHTRA	03/2016	1,142.62 -	- -	-
267	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH,MAHARASHTRA	03/2016	1,101.58 -	- -	-
268	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH,BIHAR	08/2016	1,742.01 -	12/2016 -	-
269	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH,ODISHA	03/2014	191.50 192.00	05/2016 -	-
270	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MoRTH,ODISHA	01/2015	326.63 327.00	04/2018 -	-
271	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MoRTH,ODISHA	02/2015	239.91 240.00	10/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(January 2020)
					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
272	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MoRTH,ODISHA	07/2014	342.05 342.00	01/2017 -	-
273	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH,ODISHA	08/2013	171.96 172.00	06/2016 -	-
274	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MoRTH,ODISHA	06/2016	157.30 157.00	06/2018 -	-
275	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH,UTTARAKHAND	12/2017	257.34 -	12/2019 -	-
276	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH,UTTARAKHAND	12/2017	200.34 -	12/2019 -	-
277	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MoRTH,UTTARAKHAND	12/2017	248.22 -	12/2019 -	-
278	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MoRTH,UTTARAKHAND	06/2017	282.08 -	06/2019 -	-
279	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH,UTTARAKHAND	11/2017	232.81 -	11/2019 -	-
280	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH,UTTARAKHAND	11/2017	283.51 -	11/2019 -	-
281	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH,UTTARAKHAND	11/2017	266.52 -	11/2019 -	-
282	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MoRTH,UTTARAKHAND	02/2018	293.68 -	- -	-
283	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH,UTTARAKHAND	03/2018	460.73 -	- -	-
284	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MoRTH,A & N ISLANDS	11/2017	237.80 -	11/2019 -	-
285	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH,A & N ISLANDS	11/2017	257.34 -	11/2019 -	-
286	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]MoRTH,WEST BENGAL	01/2017	396.86 396.86	09/2019 -	-
287	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH	11/2016	326.99 327.00	- -	-
288	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879]MoRTH,WEST BENGAL	03/2017	202.69 202.69	11/2019 -	-
289	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]MoRTH,WEST BENGAL	02/2018	426.18 426.18	09/2020 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(January 2020)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
290	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]MoRTH, WEST BENGAL	02/2018	218.70 218.70	11/2020 -	-
291	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) - [N24000908]MoRTH, HARYANA	01/2017	276.01 -	03/2019 07/2019	-
292	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26. - [N24000911]MoRTH, ODISHA	03/2016	165.06 -	12/2016 -	-
293	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MoRTH, ODISHA	08/2016	287.70 -	02/2017 -	-
294	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH, ODISHA	09/2016	295.67 -	02/2017 -	-
295	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH, ODISHA	12/2016	223.50 -	08/2018 -	-
296	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH, ODISHA	12/2016	206.88 -	04/2018 -	-
297	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH, ODISHA	03/2018	214.23 -	08/2018 -	-
298	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH, ODISHA	03/2018	199.16 -	08/2018 -	-
299	WIDENING FROM TWO LANE TO FOUR LANE WITH PAVED SHOULDER AND STRENGTHNING OF EXISTING PAVEMENT BETWEE - [N24000920]MoRTH, GUJARAT	03/2016	223.67 -	02/2017 -	-
300	UPGRADATION TO 2 LANE WITH PAVED SHOULDER WITH RIGID PAVEMENTS FROM 37/400 TO KM 66/700 ON NH 848 ON - [N24000921]MoRTH, GUJARAT	03/2016	208.34 -	02/2016 -	-
301	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922]MoRTH, GUJARAT	12/2017	867.97 -	11/2018 -	-
302	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEE - [N24000923]MoRTH, GUJARAT	03/2018	464.07 -	11/2018 -	-
303	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]MoRTH, GUJARAT	10/2018	400.76 -	05/2019 -	-
304	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926]MoRTH, GUJARAT	08/2017	962.43 -	03/2018 -	-
305	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH, BIHAR	09/2018	1,478.40 -	- -	-
306	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552-EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950]MoRTH, RAJASTHAN	11/2017	187.82 -	04/2018 -	-
307	NETRA VILLAGE TO MANDORE SECTION OF NH-65 KM 267+500 TO 296+070 (4L) UNDER EPC. - [N24000951]MoRTH, RAJASTHAN	10/2014	382.81 -	01/2015 -	-
308	UP-GRADATION TO TWO LANE WITH PAVED SHOULDER FOR SECTION FROM KM 58.000 TO KM 91.600 (BALOTRA TO SAN - [N24000952]MoRTH, RAJASTHAN	01/2017	179.32 -	11/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(January 2020)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
309	CONSTRUCTION OF NAGPUR BYPASS FROM EXISTING KM 166/260 TO KM 180/500 OF NH-65 ON EPC MODE. - [N24000953]MoRTH,RAJASTHAN	03/2016	155.77 -	09/2016 -	-
310	NAGPUR-BIKANER OF NH-11 (2L+PS) UNDER PPP. - [N24000954]MoRTH,RAJASTHAN	01/2012	378.07 478.73	01/2014 -	-
311	CITTORGARH-NEEMACH (4L) OF NH-79 AND NIMBAHARA PRATAPGARH (2L+PS) OF NH-113 UNDER PPP. - [N24000955]MoRTH,RAJASTHAN	10/2012	511.21 -	10/2013 -	-
312	DEVELOPMENT AND OPERATION OF BIKANER- SURATGARH SECTION OF NH-15 BY 2L+PS IN THE STATE OF RAJASTHAN - [N24000956]MoRTH,RAJASTHAN	03/2009	501.00 671.54	09/2013 -	-
313	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709 - [N24000957]MoRTH,RAJASTHAN	11/2017	163.95 -	04/2018 -	-
314	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000958]MoRTH,RAJASTHAN	02/2018	370.30 -	06/2018 -	-
315	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000959]MoRTH,RAJASTHAN	02/2018	341.79 -	05/2018 -	-
316	CONSTRUCTION OF 4 LANING BY CC PAVEMENT ON KOTA-DARAH OF NH-12 FROM 256/550 TO 289/550 UNDER EPC. - [N24000960]MoRTH,RAJASTHAN	12/2015	621.43 -	10/2016 -	-
317	UP-GRADATION TO 2 LANE WITH PAVED SHOULDER FOR SECTION FROM KM 118.900 TO KM 156.955 BALOTRA TOSANDE - [N24000961]MoRTH,RAJASTHAN	01/2017	163.54 -	07/2017 -	-
318	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH,TELANGANA	01/2017	244.54 -	05/2019 -	-
319	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]MoRTH,TELANGANA	01/2017	196.52 -	10/2019 -	-
320	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]MoRTH,TELANGANA	01/2017	283.00 -	12/2019 -	-
321	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]MoRTH,TELANGANA	01/2017	359.27 -	05/2019 -	-
322	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]MoRTH,TELANGANA	01/2018	230.03 -	12/2019 -	-
323	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH,TELANGANA	02/2018	294.13 -	11/2019 -	-
324	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH,TELANGANA	02/2018	220.28 -	11/2019 -	-
325	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH,TELANGANA	01/2017	605.08 -	10/2019 -	-
326	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH,TELANGANA	03/2018	192.67 -	07/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(January 2020)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
327	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH,TELANGANA	01/2019	193.19 -	- -	-
328	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C - [N24000999]MoRTH,BIHAR	11/2016	230.34 -	10/2019 -	-
329	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH,BIHAR	03/2018	153.24 -	- -	-
330	SARSAM TO KOTHARI - [N24001002]MoRTH,MAHARASHTRA	02/2016	545.64 -	07/2019 -	-
331	AKOLA TO AKOT - [N24001003]MoRTH,MAHARASHTRA	01/2017	313.95 -	06/2019 -	-
332	AKOT TO ANJANGAON - [N24001006]MoRTH,MAHARASHTRA	01/2017	245.77 246.00	06/2019 -	-
333	ANJANGAON TO MAH/MP BORDER - [N24001007]MoRTH,MADHYA PRADESH	01/2017	359.00 359.00	06/2019 -	-
334	MEHKAR TO CHIKALI - [N24001011]MoRTH,MAHARASHTRA	02/2017	322.48 322.00	05/2019 -	-
335	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA	01/2017	341.16 341.00	06/2019 -	-
336	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH,MAHARASHTRA	01/2017	471.61 472.00	06/2019 -	-
337	DAHEGAON TO KUHI - [N24001017]MoRTH,MAHARASHTRA	01/2017	228.89 229.00	06/2019 -	-
338	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA	01/2017	392.83 393.00	06/2019 -	-
339	JINTUR TO PARBHANI - [N24001039]MoRTH,MAHARASHTRA	01/2017	356.66 356.66	- -	-
340	KALMAB TO RALEGAON - [N24001044]MoRTH,MAHARASHTRA	01/2017	467.78 -	06/2019 -	-
341	RALEGAON TO RAMTIRTH - [N24001046]MoRTH,MAHARASHTRA	01/2017	210.81 -	07/2019 -	-
342	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA	01/2017	232.77 -	07/2019 -	-
343	HELWAK TO KARAD - [N24001055]MoRTH,MAHARASHTRA	02/2017	416.99 -	07/2019 -	-
344	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA	02/2017	422.02 422.00	07/2019 -	-
345	BODHWAD TO STATE BORDER - [N24001086]MoRTH,MAHARASHTRA	01/2017	178.26 -	07/2019 -	-
346	KOLDE TO KHETIYA - [N24001090]MoRTH,MAHARASHTRA	01/2017	509.18 -	07/2019 -	-
347	SATARA TO MHASWAD - [N24001092]MoRTH,MAHARASHTRA	01/2017	653.46 -	07/2019 -	-
348	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA	01/2017	388.44 -	- -	-
349	MHASWAD TO TEMBHURNI - [N24001099]MoRTH,MAHARASHTRA	01/2017	488.60 -	07/2019 -	-
350	KURUDWADI TO PANDHARPUR - [N24001101]MoRTH,MAHARASHTRA	01/2017	307.63 -	07/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(January 2020)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
351	PANDHARPUR TO SANGOLA - [N24001102]MoRTH,MAHARASHTRA	07/2017	218.38 -	07/2019 -	-
352	SARAD VANI PIMPALGAON - [N24001103]MoRTH,MAHARASHTRA	01/2017	250.46 -	07/2019 -	-
353	CHIMUR TO WARORA - [N24001105]MoRTH,MAHARASHTRA	11/2016	467.70 -	03/2019 -	-
354	GADCHIROLI TO MUL - [N24001116]MoRTH,MAHARASHTRA	12/2016	484.15 -	06/2019 -	-
355	NAGBHID TO ARMORI - [N24001119]MoRTH,MAHARASHTRA	09/2016	269.05 -	07/2019 -	-
356	PAITHAN TO SHIRUR - [N24001122]MoRTH,MAHARASHTRA	03/2017	341.80 -	06/2019 -	-
357	SHIRUR TO KHARDA - [N24001123]MoRTH,MAHARASHTRA	02/2017	381.77 -	06/2019 -	-
358	AURANGABAD TO SILLOD - [N24001124]MoRTH,MAHARASHTRA	02/2017	456.32 -	06/2019 -	-
359	SILLOD TO FARDAPUR - [N24001125]MoRTH,MAHARASHTRA	02/2017	337.46 -	06/2019 -	-
360	FARDAPUR TO JALGAON - [N24001126]MoRTH,MAHARASHTRA	02/2017	456.45 -	06/2019 -	-
361	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA	02/2017	406.51 -	06/2019 -	-
362	BHOKAR TO SARSAM - [N24001128]MoRTH,MAHARASHTRA	02/2017	295.09 -	07/2019 -	-
363	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND	08/2016	234.88 -	12/2017 -	-
364	PARSHURAM GHAT TO ARAWALI - [N24001133]MoRTH,MAHARASHTRA	04/2016	983.14 983.00	12/2019 -	-
365	KANTE TO WAKED - [N24001134]MoRTH,MAHARASHTRA	03/2016	1,230.02 1,230.00	11/2019 -	-
366	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	-
367	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT - [N24001154]MoRTH,KARNATAKA	08/2016	367.44 -	01/2017 -	-
368	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT - [N24001155]MoRTH,KARNATAKA	08/2016	175.20 -	01/2017 -	-
369	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS - PA - [N24001156]MoRTH,KARNATAKA	01/2017	166.67 -	09/2017 -	-
370	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA	08/2016	175.50 -	02/2017 -	-
371	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA	03/2018	159.97 -	06/2019 -	-
372	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]MoRTH,KARNATAKA	01/2018	159.70 -	07/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(January 2020)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
373	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA	09/2017	191.60 -	10/2018 -	-
374	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH - - [N24001161]MoRTH,KARNATAKA	12/2017	297.30 -	01/2019 -	-
375	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA	03/2018	325.86 -	10/2018 -	-
376	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]MoRTH,KARNATAKA	08/2016	329.01 -	02/2017 -	-
377	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA	10/2016	396.96 -	03/2017 -	-
378	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA	11/2016	314.90 -	03/2017 -	-
379	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA	03/2015	159.12 -	01/2016 -	-
380	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776) - [N24001167]MoRTH,KARNATAKA	03/2015	165.67 -	01/2016 -	-
381	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM. - [N24001170]MoRTH,KARNATAKA	01/2014	471.16 -	08/2014 -	-
382	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA	01/2017	291.49 -	08/2017 -	-
383	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND	11/2016	336.25 -	09/2019 -	-
384	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S - [N24001183]MoRTH,ANDHRA PRADESH	07/2014	251.55 -	02/2015 -	-
385	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MoRTH,RAJASTHAN	03/2019	178.13 -	- -	-
386	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR	02/2019	2,926.42 -	- -	-
387	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH,UTTAR PRADESH	03/2018	306.59 -	- -	-
388	IMPROVEMENT AND UP-GRADATION OF EXISITING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH,UTTAR PRADESH	11/2018	281.45 -	- -	-
389	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]MoRTH,CHHATISGARH	01/2016	497.14 -	08/2016 -	-
390	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218]MoRTH,CHHATISGARH	11/2015	335.32 -	06/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (January 2020)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
391	REHABILITATION AND UPGADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]MoRTH,CHHATISGARH	01/2016	476.20 544.00	09/2016 -	-
392	REHABILITATION AND UPGADATION OF NH 200 FROM KM 127.500 TO 178.944 DARRIGHAT TO BANARI SECTION - [N24001220]MoRTH,CHHATISGARH	03/2016	491.52 -	09/2016 -	-
393	REHABILITATION AND UPGADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]MoRTH,CHHATISGARH	01/2016	624.98 -	10/2016 -	-
394	REHABILITATION AND UPGADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222]MoRTH,CHHATISGARH	03/2016	452.94 -	07/2016 -	-
395	WIDENING OF SL TO 2 L KM. 107-184.80 SUKUMA TO KONTA ON NH 221 - [N24001223]MoRTH,CHANDIGARH	03/2010	179.89 271.00	03/2013 -	-
396	REHABILITATION AND UPGADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO - [N24001224]MoRTH,CHHATISGARH	03/2017	423.79 -	01/2018 -	-
397	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1 - [N24001225]MoRTH,CHANDIGARH	12/2010	169.26 299.00	01/2019 -	-
398	REHABILITATION AND UPGADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226]MoRTH,CHHATISGARH	12/2014	496.02 -	03/2015 -	-
399	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228]MoRTH,CHHATISGARH	11/2017	188.80 -	05/2019 -	-
400	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 - [N24001229]MoRTH,CHHATISGARH	12/2014	379.16 -	11/2017 -	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>				
401	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH	07/2015	197.16 197.16	10/2018 09/2015	09/2018
402	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL,ARUNACHAL PRADESH	10/2015	210.50 210.50	- 01/2016	01/2019
403	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL,ARUNACHAL PRADESH	03/2015	194.11 -	05/2018 -	08/2019
404	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM	04/2017	519.09 -	09/2019 -	09/2019
405	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM	04/2017	640.07 -	09/2019 -	09/2019
406	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM	04/2017	642.96 -	09/2019 -	09/2019
407	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM	04/2017	473.18 -	09/2019 -	09/2019

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(January 2020)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
408	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM	04/2017	537.82 -	09/2019 -	09/2019
409	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM	04/2017	518.53 -	09/2019 -	09/2019
410	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM	04/2017	404.29 -	09/2019 -	09/2019
411	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM	04/2017	428.11 -	09/2019 -	09/2019
412	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH	04/2016	198.00 -	10/2016 -	10/2019
413	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL,ASSAM	06/2016	829.00 -	01/2019 -	-
414	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM	03/2015	168.39 -	11/2018 -	-
415	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM	10/2014	588.95 -	11/2018 -	-
416	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL,ARUNACHAL PRADESH	10/2015	179.82 -	01/2019 -	-
417	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA	10/2014	369.00 -	03/2018 12/2019	-
418	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]NHIDCL,ASSAM	12/2015	225.02 -	12/2018 -	-
419	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM	12/2015	223.30 -	06/2018 -	-
420	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-
421	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM	12/2015	289.99 -	12/2018 -	-
422	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM	01/2016	252.00 -	01/2016 12/2021	-
423	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450 TO KM 605.600(EXISTING CHAINAGE FROMKM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH	01/2016	183.65 -	11/2016 -	-
424	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH	02/2017	195.23 -	04/2017 -	-
425	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH	02/2017	203.36 -	04/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(January 2020)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
426	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH	01/2017	194.66 -	04/2017 -	-
427	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND	02/2017	507.68 -	04/2017 -	-
428	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH	01/2017	198.22 -	04/2017 -	-
429	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM	04/2017	388.00 -	10/2017 -	-
430	CONSTRUCTION AND UPGRADE OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND	03/2018	274.31 -	05/2018 -	-
431	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND	03/2018	403.36 -	06/2018 -	-
432	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND	03/2018	417.24 -	05/2018 -	-
433	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS	03/2015	262.97 -	10/2018 -	-
434	2 LANE WITH HARD SHOULDER , REHABILITATION AND UPGRADE OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS	03/2017	409.85 -	12/2017 -	-
435	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS	03/2015	277.17 -	04/2017 -	-
436	REHABILITATION AND UPGRADE OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS	02/2018	391.00 -	10/2018 -	-
437	REHABILITATION AND UPGRADE OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS	03/2018	234.27 -	10/2018 -	-
438	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND	03/2018	500.09 336.49	09/2018 -	-
439	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND	03/2018	339.57 233.35	09/2018 07/2019	-
440	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND	03/2018	239.30 174.70	09/2018 05/2019	-
441	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND	03/2018	285.68 -	09/2018 -	-
442	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND	03/2018	315.03 -	09/2018 -	-
443	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND	03/2018	240.64 -	09/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(January 2020)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
444	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND	03/2018	237.72 136.73	09/2018 11/2018	-
445	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND	03/2018	251.97 160.10	09/2018 11/2018	-
446	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND	03/2018	282.98 192.60	09/2018 11/2018	-
447	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND	03/2018	215.12 -	09/2018 -	-
448	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND	03/2018	215.79 -	09/2018 -	-
449	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND	03/2018	272.89 -	09/2018 -	-
450	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND	03/2018	323.98 -	09/2018 -	-
451	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA - [N24000766]NHIDCL,SIKKIM	04/2017	318.42 -	11/2017 -	-
452	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM	03/2017	375.80 -	- -	-
453	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM	11/2017	290.05 -	11/2017 -	-
454	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM	03/2018	264.84 -	06/2018 -	-
455	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITA AND PANITNAKI I - [N24000770]NHIDCL,WEST BENGAL	03/2017	158.65 -	06/2018 -	-
456	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM	03/2015	829.00 -	01/2016 -	-
457	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL,UTTARAKHAND	03/2018	1,383.78 -	07/2018 -	-
458	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866]NHIDCL,JAMMU AND KASHMIR	03/2018	404.17 -	08/2018 -	-
459	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM - [N24000867]NHIDCL,JAMMU AND KASHMIR	03/2018	216.00 -	11/2018 -	-
460	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR	03/2018	253.44 -	07/2019 -	-
461	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA	03/2019	306.28 -	05/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(January 2020)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
462	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH	12/2016	200.44 -	- -	-
463	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH	03/2017	1,718.59 -	- -	-
464	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 37.500 TO KM - [N24000947]NHIDCL,ARUNACHAL PRADESH	05/2016	259.52 -	- -	-
465	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH	09/2016	568.92 -	- -	-
466	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH	12/2016	188.78 -	- -	-
467	BORDUMSA NAMCHIK (BURIDEHING - JAIRAMPUR) ROAD ON NH-52B (NEW NH-215) FROM KM. 0.15 (STARTING CHAIN - [N24000977]NHIDCL,ARUNACHAL PRADESH	07/2015	189.91 -	- -	-
468	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN - [N24000978]NHIDCL,ARUNACHAL PRADESH	03/2015	172.75 -	- -	-
469	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI - [N24000979]NHIDCL,ARUNACHAL PRADESH	01/2017	256.66 -	- -	-
470	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8 - [N24001184]NHIDCL,DELHI	07/2017	269.69 -	09/2019 -	-
471	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL,ASSAM	03/2017	1,049.51 -	- -	-
<u>National Highways Authority Of India</u>					
472	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	04/2019
473	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH	08/2016	227.49 -	01/2019 -	12/2019
474	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 255.23	11/2008 01/2011	08/2013
475	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 435.78	11/2008 07/2011	01/2014
476	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- 06/2015	06/2015
477	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- 06/2015	06/2015
478	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	10/2017
479	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 03/2018	03/2018
480	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	04/2018 08/2018	08/2018
481	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 655.17	07/2009 10/2018	10/2018

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(January 2020)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
482	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA	09/2016	1,004.67 -	05/2019 -	02/2019
483	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 -	03/2019
484	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 -	06/2019
485	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 725.87	02/2019 -	06/2019
486	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 520.00	02/2009 07/2019	07/2019
487	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	04/2010 -	07/2019
488	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	11/2017 -	07/2019
489	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 340.14	04/2009 03/2011	08/2019
490	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 -	09/2019
491	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 -	06/2019 12/2016	09/2019
492	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	06/2019 -	09/2019
493	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	06/2019 -	09/2019
494	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 767.03	08/2018 -	09/2019
495	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT	12/2016	417.19 -	- -	09/2019
496	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	09/2019
497	TWO LANING WITH PAVED SHOULDER OF KARAU - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 09/2014	10/2019
498	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	05/2018 10/2019	10/2019
499	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH	06/2015	1,583.79 -	01/2019 10/2019	10/2019
500	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	05/2018 03/2018	10/2019
501	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	- 02/2016	10/2019
502	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 537.16	07/2018 -	11/2019
503	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN	06/2016	763.23 -	06/2019 -	11/2019
504	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	04/2019 -	11/2019

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(January 2020)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
505	JUNAGADH BYPASS - [N24000701]NHAI, GUJARAT	10/2017	232.49 -	10/2017 -	11/2019
506	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI, KARNATAKA	09/2010	946.00 -	06/2018 -	12/2019
507	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI, KERALA	02/2010	617.00 -	08/2012 -	12/2019
508	4 LANING OF AMBALA - KATHAL - PACKAGE -1 - [N24000443]NHAI, HARYANA	12/2015	602.95 507.70	06/2016 -	12/2019
509	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI, MADHYA PRADESH	03/2015	794.30 637.86	- -	12/2019
510	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI, BIHAR	12/2015	1,167.45 -	- -	12/2019
511	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI, JHARKHAND	07/2016	458.03 -	- 12/2017	12/2019
512	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI, MAHARASHTRA	01/2017	244.90 -	05/2019 -	12/2019
513	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT	03/2010	1,509.10 3,787.21	09/2012 12/2019	-
514	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI, MULTI STATE	02/2009	1,693.75 2,848.49	08/2011 -	-
515	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI, MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	-
516	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI, MULTI STATE	02/2011	2,498.76 -	08/2014 -	-
517	INDORE-DEWAS(NH-3) - [N24000159]NHAI, MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-
518	NASHRI- CHANANI - [N24000162]NHAI, JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-
519	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-
520	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-
521	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI, TAMIL NADU	05/2010	374.00 -	05/2013 -	-
522	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI, TAMIL NADU	09/2011	485.00 -	08/2013 -	-
523	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI, ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-
524	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, BIHAR	09/2011	574.00 -	03/2014 -	-
525	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, BIHAR	10/2011	375.09 -	04/2014 -	-
526	PANIKHOLI-RIMOLI - [N24000197]NHAI, ODISHA	03/2012	1,410.00 -	09/2014 -	-
527	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI, UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	-
528	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH	07/2012	291.36 -	01/2014 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(January 2020)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
529	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	-
530	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	06/2015 -	-
531	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-
532	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 2,125.24	12/2015 -	-
533	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	02/2014 -	-
534	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	-
535	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	09/2016 -	-
536	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA	08/2015	723.54 1,286.84	02/2018 10/2017	-
537	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	-
538	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	01/2016 -	-
539	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH	06/2014	301.04 -	01/2016 -	-
540	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	01/2016 -	-
541	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	05/2019 -	-
542	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	05/2019 -	-
543	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	04/2018 -	-
544	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	04/2019 -	-
545	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	01/2019 -	-
546	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-
547	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 -	06/2018 -	-
548	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-
549	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	-
550	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	04/2019 -	-
551	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	- -	-
552	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA	11/2015	867.66 1,464.24	05/2018 02/2018	-
553	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(January 2020)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
554	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	-
555	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	-
556	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	- -	-
557	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	04/2019 -	-
558	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	- -	-
559	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR	08/2015	516.13 -	04/2018 -	-
560	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-
561	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 151.11	07/2018 -	-
562	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	04/2019 -	-
563	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	11/2018 -	-
564	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 3,267.94	- 03/2017	-
565	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 -	03/2019 -	-
566	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-
567	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	04/2019 -	-
568	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	- -	-
569	FOUR LANING OF TALAJA - MAHUA SECTION OF NH - 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT	05/2016	834.64 -	- -	-
570	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	- -	-
571	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	- -	-
572	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 241.41	- -	-
573	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	10/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (January 2020)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
574	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI, RAJASTHAN	08/2016	320.30 -	01/2019 -	-
575	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI, ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-
576	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI, UTTAR PRADESH	01/2017	450.68 -	- -	-
577	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI, MADHYA PRADESH	09/2017	374.40 -	09/2017 -	-
578	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI, MADHYA PRADESH	12/2017	950.27 -	- -	-
579	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI, BIHAR	12/2017	2,598.00 -	- -	-
580	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI, ANDHRA PRADESH	12/2017	328.67 -	- -	-
581	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI, ANDHRA PRADESH	12/2017	357.00 -	- -	-
582	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI, UTTAR PRADESH	12/2017	305.00 -	- -	-
583	REHABILITATION AND UPGRADE OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI, BIHAR	01/2018	573.70 -	- -	-
584	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI, BIHAR	01/2018	895.39 -	- -	-
585	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI, JHARKHAND	01/2018	273.46 -	- -	-
586	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI, JHARKHAND	01/2018	1,155.16 -	- -	-
587	FOUR LANING OF DELINKED STRETCH OF SEONI - MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI, MADHYA PRADESH	01/2018	960.24 -	- -	-
588	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI, MADHYA PRADESH	01/2018	770.73 -	- -	-
589	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI, ODISHA	01/2018	633.68 -	- -	-
590	VARANASI RING ROAD PKG - I - [N24000740]NHAI, UTTAR PRADESH	01/2018	450.77 929.89	- -	-
591	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI, TELANGANA	03/2017	4,429.00 -	03/2017 -	-
592	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI, KARNATAKA	02/2018	486.78 -	- -	-
593	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI, KERALA	02/2018	1,424.77 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(January 2020)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
594	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 -	- -	-
595	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 2,283.50	- 10/2019	-
596	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 1,065.70	- -	-
597	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH	03/2018	925.40 1,197.00	- -	-
598	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN	02/2018	741.86 -	- -	-
599	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN	02/2018	716.76 -	- -	-
600	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	-
601	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 1,332.00	- -	-
602	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH	03/2018	1,025.80 -	- -	-
603	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH	03/2018	1,115.28 -	- -	-
604	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K - [N24000804]NHAI,TELANGANA	03/2018	802.65 -	- -	-
605	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-
606	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	- -	-
607	FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA	03/2018	950.63 -	- -	-
608	FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA	03/2018	857.62 -	- -	-
609	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI,TELANGANA	03/2018	828.29 998.89	- 11/2019	-
610	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU	03/2018	633.55 -	- -	-
611	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU	03/2018	2,065.96 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (January 2020)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
612	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE	03/2018	1,294.47 -	- -	-
613	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE	03/2018	998.70 -	- -	-
614	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN	03/2018	874.25 -	- -	-
615	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN	03/2018	1,158.35 -	- -	-
616	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB	03/2018	199.90 149.90	- -	-
617	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH – 14 - [N24001185]NHAI,UTTAR PRADESH	11/2017	2,159.00 -	01/2019 -	-
618	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI,HARYANA	01/2019	1,051.91 -	- -	-
619	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI,HARYANA	01/2019	1,120.06 -	- -	-
620	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA	01/2019	1,137.42 -	- -	-
621	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA	01/2019	1,033.19 -	- -	-
622	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA	01/2019	1,243.45 -	- -	-
623	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA	01/2019	889.36 -	- -	-
624	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA	01/2019	1,018.79 -	- -	-
625	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA	01/2019	996.65 -	- -	-
626	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI,MADHYA PRADESH	10/2019	743.88 -	- -	-
627	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]NHAI,MADHYA PRADESH	12/2017	656.98 -	- -	-
628	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA - [N24001213]NHAI,MADHYA PRADESH	12/2017	1,094.97 -	- -	-
629	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214]NHAI,MADHYA PRADESH	12/2017	217.96 -	- -	-
630	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 275.00	05/2017 -	-
631	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	12/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(January 2020)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
632	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 1,444.25	- 02/2019	-
	Total		2,81,460.97 -		
	<u>TELECOMMUNICATIONS</u>				
	<u>Indian Telephone Industry</u>				
633	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI,MULTI STATE	09/2014	2,111.17 -	09/2014 -	-
	<u>Mahanagar Telephone Nigam Limited</u>				
634	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI	06/2016	418.26 -	06/2017 -	-
	Total		2,529.43 -		
	<u>URBAN DEVELOPMENT</u>				
	<u>Central Public Works Department</u>				
635	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	03/2012 -	12/2019
636	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	11/2014 -	-
637	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	12/2015 -	-
638	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	12/2013 -	-
639	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP - [N28000108]CPWD,ANDHRA PRADESH	01/2018	206.58 -	03/2019 -	-
640	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI - [N28000123]CPWD,DELHI	07/2017	218.72 218.72	- -	-
641	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130]CPWD,JAMMU AND KASHMIR	03/2019	329.00 -	- -	-
642	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]CPWD,JAMMU AND KASHMIR	01/2018	676.00 -	- -	-
	<u>Chennai Metro Rail Ltd</u>				
643	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 -	12/2015 -	-
	<u>Delhi Metro Rail Corporation</u>				
644	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	03/2016 -	-
	<u>Hindustan Steelwork Construction Limited</u>				
645	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	12/2015 -	-
646	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	12/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(January 2020)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
647	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	12/2016 -	-
648	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,070.97	02/2014 -	-
649	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 324.87	12/2015 -	-
650	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	09/2017 -	-
651	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	- -	-
652	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL,GUJARAT	01/2013	175.00 -	- -	-
653	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	03/2017 -	-
654	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 253.92	06/2016 -	-
655	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND	12/2007	200.00 -	03/2018 -	-
656	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	12/2016 -	-
657	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND	04/2013	170.00 -	04/2018 -	-
658	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL	08/2012	185.37 -	03/2016 -	-
	<u>Jawahar Lal Nehru National Urban Renewal Mission</u>				
659	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-
	<u>Lucknow Metro Rail Corporation Limited</u>				
660	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	-
	<u>Nagpur Metro Rail Corporation Ltd</u>				
661	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	12/2019
	<u>National Building Construcion Corporation Ltd</u>				
662	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI	07/2016	2,694.00 -	- -	-
	Total		78,604.08 -		
	<u>WATER RESOURCES</u>				
	<u>Brahmaputra Board</u>				
663	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPB,MAHARASHTRA	03/2017	233.57 -	12/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(January 2020)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>Uttarakhand Pey Jal Nigam</u>				
664	INTERCEPTION AND DIVERSION (I&D)WITH STP AT RISHIKESH - [N30000004]UKJalNigam,UTTARAKHAND	03/2017	158.00 -	11/2019 -	-
	Total		391.57 -		
	<u>HUMAN RESOURCE DEVELOPMENT</u>				
	<u>Edcil(India) Limited</u>				
665	STUDY IN INDIA - [N42000003]EDCIL,MULTI STATE	03/2018	150.00 -	04/2018 -	-
	<u>Indian Institute Of Technology, Kharagpur</u>				
666	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION - [N42000004]IITKGP,MULTI STATE	08/2018	418.00 -	03/2019 -	-
	Total		568.00 -		
	Grand Total		4,55,034.41		

Details of Projects Without Original Date of Commissioning

Annexure - IX

Costing Rs. 150 Crore and above (January 2020)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>COAL</u>								
	<u>Singareni Colliers Company Limited</u>								
1	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL, TELANGANA	11/2016	272.73 -	272.73	153.75	- 04/2017	03/2020	35(R3)	1/6
2	RAMPURAM SHAFT BLOCK - [N06000174]SCCL, TELANGANA	08/2016	431.92 -	431.92	-	- 03/2023	-	-	0/9
3	SRAVANAPALLI OPENCAST PROJECT - [N06000175]SCCL, TELANGANA	02/2018	412.70 -	412.70	.76	- 03/2023	-	-	0/7
	Total		1,117.35 -	1,117.35	154.51				1/22
	<u>PETROLEUM</u>								
	<u>Indian Oil Corporation Limited</u>								
4	LPG BP PROJECT JODHPUR - [N16000318]IOCL, RAJASTHAN	03/2018	229.80 -	229.80	74.47	- -	03/2021	-	13/26
5	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT - [N16000336]IOCL, GUJARAT	03/2018	588.20 -	588.20	1.24	- -	08/2022	-	9/17
	Total		818.00 -	818.00	75.71				22/43
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Hospital Services Consultancy Corporation Ltd</u>								
6	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC, UTTAR PRADESH	03/2018	268.84 -	268.84	181.36	- -	04/2020	-	0/0
7	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC, DELHI	12/2017	156.56 -	156.64	80.28	- -	05/2020	-	0/0
8	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC, GOA	01/2018	249.01 -	249.07	149.26	- -	05/2020	-	0/0
9	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC, MAHARASHTRA	03/2018	582.99 -	582.99	268.43	- -	06/2020	-	0/0
10	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC, ANDHRA PRADESH	03/2018	601.02 -	601.02	219.05	- -	07/2020	-	0/0
11	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC, WEST BENGAL	04/2018	651.99 -	651.99	285.33	- -	07/2020	-	0/0
	Total		2,510.41 -	2,510.55	1,183.71				0/0
	<u>RAILWAYS</u>								
	<u>East Central Railways</u>								

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above

(January 2020)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
12	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 367.17	440.00	432.20	- -	01/2020	-	0/1
13	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR,JHARKHAND	03/1999	1,033.07 3,020.95	3,376.00	3,349.65	- -	03/2021	-	0/0
14	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 1,625.87	1,625.87	544.36	- -	03/2021	-	0/0
15	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR	04/1999	325.00 735.20	735.20	367.62	- -	03/2021	-	0/0
16	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 1,470.50	1,470.50	849.10	- -	03/2021	-	0/0
17	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]ECR,BIHAR	04/1991	329.39 803.11	1,483.14	1,060.33	- -	12/2021	-	0/0
18	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 614.45	614.45	311.33	- -	03/2022	-	0/0
19	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR	04/2006	378.56 -	1,858.75	377.77	- -	03/2022	-	0/0
20	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 519.33	519.33	195.83	- -	02/2023	-	0/0
21	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 2,066.78	2,066.78	1,454.19	- -	03/2023	-	0/0
22	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	1,605.17 1,605.17	1,605.17	23.55	- 03/2023	03/2023	0(R3)	0/0
23	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR	04/2008	326.20 -	2,995.01	1.94	- -	03/2024	-	0/0
24	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	228.05	1.53	- -	03/2024	-	0/0
	<u>Eastern Railways</u>								
25	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	402.48	402.48	- -	03/2020	-	0/0
26	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	260.83	260.83	- -	03/2021	-	0/0
27	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	272.20	196.05	- -	09/2021	-	0/0
28	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	310.70	287.10	- -	03/2024	-	0/0
29	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	1,261.34	-	- -	03/2025	-	0/0
30	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	260.10	10.73	- -	03/2025	-	0/0
31	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	174.56	71.42	- -	03/2025	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (January 2020)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
32	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	250.55	20.12	- -	03/2025	-	0/0
33	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	527.54	1.76	- -	03/2025	-	0/0
34	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	298.22	52.09	- -	03/2025	-	0/0
35	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	336.96	70.20	- -	03/2025	-	0/0
36	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	166.89	.02	- -	03/2025	-	0/0
<u>Metropolitan Rapid Transport Projects</u>									
37	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	268.52	.03	- -	03/2025	-	0/0
<u>North East Frontier Railway</u>									
38	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 -	373.87	273.20	- -	06/2021	-	0/0
39	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	333.76 -	360.00	6.74	- 03/2022	03/2022	0(R3)	0/0
40	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 -	380.00	38.18	- 03/2022	03/2022	0(R3)	0/0
<u>Northern Railway</u>									
41	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	346.63	233.23	- -	06/2020	-	0/0
42	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	791.39	517.05	- -	03/2022	-	0/0
43	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	295.68	92.91	- -	03/2023	-	0/0
44	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	1,229.00 -	1,230.00	103.72	- -	03/2023	-	0/0
45	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	197.17	106.97	- -	03/2024	-	0/0
46	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	841.90	1.73	- -	03/2024	-	0/0
<u>Rail Vikas Nigam Ltd.</u>									
47	RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE	04/2007	2,062.30 2,062.30	2,062.30	932.12	- -	03/2025	-	2/2
<u>South East Central Railway</u>									
48	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 1,473.76	1,413.76	1,351.73	- 01/2020	01/2020	0(R3)	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (January 2020)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>South Eastern Railway</u>								
49	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	620.00	40.99	- 03/2025	03/2025	0(R3)	0/0
	<u>South Western Railway</u>								
50	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR, KARNATAKA	04/2011	1,801.01 1,801.01	1,801.01	57.70	- -	12/2023	-	0/0
51	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR, KARNATAKA	04/2013	558.00 692.43	692.43	-	- -	12/2023	-	0/0
52	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR, MULTI STATE	04/2013	296.00 466.65	466.65	-	- -	12/2023	-	0/0
53	WHITE FIELD-KOLAR NL - [N22000280]SWR, KARNATAKA	04/2011	348.85 348.85	348.85	.36	- -	12/2023	-	0/0
54	TORANAGALLU-RANJITPURA DL - [N22000298]SWR, KARNATAKA	04/2011	146.75 146.75	167.50	.34	- -	12/2023	-	0/0
55	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR, KARNATAKA	04/2013	327.25 367.77	367.77	-	- -	12/2023	-	0/0
56	HUBLI-ANKOLA(NL), SWR - [220100193]SWR, KARNATAKA	04/1997	2,315.00 -	2,315.00	151.40	- -	12/2024	-	0/0
	<u>Southern Railway</u>								
57	MADURAI-BODINAYAKKANUR - [N22000201]SR, TAMIL NADU	04/2008	164.41 -	450.00	197.11	- -	03/2020	-	0/0
58	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR, TAMIL NADU	04/2007	931.98 -	951.24	753.41	- -	03/2020	-	0/0
	<u>Western Railway</u>								
59	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR, GUJARAT	04/2011	844.10 844.10	844.10	110.71	- 03/2021	03/2021	0(R3)	0/0
	Total		23,987.95 -	41,126.39	15,311.83				2/3
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>								
60	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH, MADHYA PRADESH	06/2015	390.51 -	390.51	209.67	- -	03/2020	-	0/0
61	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH, ARUNACHAL PRADESH	11/2016	243.89 -	243.89	128.46	- -	09/2020	-	0/0
62	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]MoRTH, PUNJAB	11/2015	889.24 904.82	904.82	739.41	- 05/2020	-	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (January 2020)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
63	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MORTH, ARUNACHAL PRADESH	09/2011	1,979.00 -	1,979.00	1,189.58	- 03/2020	-	-	0/0
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
64	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL, ASSAM	10/2017	818.00 -	818.00	63.08	- -	06/2020	-	0/4
65	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL, ARUNACHAL PRADESH	04/2016	245.79 -	245.79	129.43	- -	09/2020	-	2/4
66	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL, ARUNACHAL PRADESH	11/2015	434.06 -	434.06	172.89	- -	12/2020	-	2/4
67	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D - [N24000974]NHIDCL, ARUNACHAL PRADESH	02/2017	199.02 199.02	199.02	13.82	- 02/2018	02/2021	36(R3)	0/0
68	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D - [N24000975]NHIDCL, ARUNACHAL PRADESH	02/2017	184.88 184.88	184.88	7.68	- 02/2018	02/2021	36(R3)	0/0
69	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL, MEGHALAYA	04/2017	553.51 -	553.51	44.39	- -	09/2021	-	0/4
70	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL, ARUNACHAL PRADESH	02/2017	175.06 175.06	175.06	29.08	- 04/2019	04/2022	36(R3)	0/0
71	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL, ARUNACHAL PRADESH	02/2017	176.12 176.12	176.12	28.16	- 04/2019	04/2022	36(R3)	0/0
	<u>National Highways Authority Of India</u>								
72	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL	10/2015	361.15 -	361.15	186.64	- -	01/2020	-	0/0
73	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI, BIHAR	08/2015	814.04 -	825.17	646.72	- -	01/2020	-	2/3
74	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI, KERALA	06/2015	845.24 -	941.00	859.59	- -	01/2020	-	0/0
75	4-LANING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI, UTTAR PRADESH	03/2016	1,668.00 -	1,668.00	946.08	- -	01/2020	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (January 2020)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
76	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	829.97	194.67	- -	01/2020	-	0/0
77	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB	03/2018	196.05 149.90	196.05	143.03	- -	01/2020	-	0/0
78	MEERUT-BULANDSHAHAH - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 868.77	987.94	727.69	- 10/2019	02/2020	4(R3)	0/2
79	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	1,443.00	1,246.85	- -	02/2020	-	0/0
80	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 881.00	688.70	870.48	- 05/2017	02/2020	33(R3)	0/0
81	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	1,244.10	1,445.00	- -	02/2020	-	0/0
82	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 659.57	677.72	659.57	- -	03/2020	-	0/0
83	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	1,069.65	546.51	- -	03/2020	-	0/0
84	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 315.00	315.00	246.70	- 03/2020	03/2020	0(R3)	0/0
85	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	379.90	125.68	- -	03/2020	-	0/0
86	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA	03/2018	275.12 -	275.12	134.80	- -	03/2020	-	0/0
87	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTING - [N24000837]NHAI,HARYANA	03/2018	307.79 -	307.79	160.12	- -	03/2020	-	0/0
88	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA	03/2018	198.05 -	198.05	103.34	- -	03/2020	-	0/0
89	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA	03/2018	551.58 -	551.58	305.46	- -	03/2020	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (January 2020)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
90	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	1,737.00	1,159.07	- -	04/2020	-	0/0
91	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 1,367.00	1,169.61	1,203.12	- -	04/2020	-	0/0
92	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN	09/2016	1,239.82 -	1,239.82	1,427.14	- -	05/2020	-	3/4
93	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	1,145.31	1,045.00	- -	05/2020	-	0/0
94	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 3,207.63	1,087.00	562.94	- 02/2018	05/2020	27(R3)	0/0
95	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	479.00	453.80	- -	06/2020	-	0/0
96	CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	557.30	211.24	- 06/2020	06/2020	0(R3)	0/0
97	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA	03/2018	181.78 -	181.78	76.56	- -	06/2020	-	0/0
98	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	1,408.00	442.70	- -	07/2020	-	0/0
99	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	1,273.71	581.40	- -	07/2020	-	0/0
100	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	392.00	286.99	- -	08/2020	-	0/0
101	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	447.75	1,028.99	- -	08/2020	-	0/0
102	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE-- [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	1,031.95	367.00	- -	08/2020	-	0/0
103	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	1,583.18	271.06	- -	09/2020	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (January 2020)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
104	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN	02/2018	1,103.88 -	1,103.88	404.43	- -	09/2020	-	0/0
105	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	681.67	402.94	- -	10/2020	-	1/2
106	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	720.00	343.72	- 10/2020	10/2020	0(R3)	0/0
107	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 448.18	448.18	193.77	- -	10/2020	-	0/0
108	FOUR LANING OF CHETTICKULAM TO NATHAM SECTION OF NH-785 FROM CHETTICKULAM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35 -	505.35	100.44	- -	11/2020	-	0/0
109	FOUR LANING OF MADURAI- CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICKULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	628.71	120.55	- -	11/2020	-	0/0
110	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53 -	291.53	68.92	- 11/2020	11/2020	0(R3)	0/0
111	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21 -	289.21	41.34	- -	11/2020	-	0/0
112	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWA (KM 283.500 OF NH 65 NAGPUR ROAD) SECTION - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	1,308.73	99.68	- -	12/2020	-	0/0
113	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFAR - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	207.00	34.77	- 03/2020	12/2020	9(R3)	0/0
114	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43 -	314.43	46.12	- -	12/2020	-	0/0
115	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA	03/2018	1,484.30 -	1,484.30	133.06	- -	12/2020	-	0/0
116	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA	03/2018	642.13 -	807.00	395.79	- -	12/2020	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (January 2020)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
117	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	1,251.11	1,084.26	- -	01/2021	-	0/0
118	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR	12/2017	1,471.75 1,339.00	1,339.00	588.87	- -	01/2021	-	1/3
119	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB	02/2018	261.76 -	207.00	112.77	- -	01/2021	-	0/0
120	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT	02/2018	1,052.21 1,449.00	1,449.00	342.39	- -	01/2021	-	0/0
121	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT	03/2018	2,702.05 -	2,043.00	-	- 05/2018	01/2021	32(R3)	0/0
122	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26 -	1,166.26	163.29	- -	02/2021	-	0/0
123	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH	03/2018	565.09 -	565.09	191.77	- -	02/2021	-	0/0
124	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	1,282.94	288.42	- -	03/2021	-	0/0
125	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	1,008.96	595.10	- -	03/2021	-	0/0
126	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH	03/2018	1,029.96 -	1,261.05	97.55	- 03/2021	03/2021	0(R3)	0/0
127	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 1,073.10	1,005.08	-	- 03/2019	03/2021	24(R3)	0/0
128	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA	01/2018	621.00 565.02	621.00	383.83	- 10/2018	04/2021	30(R3)	2/3
129	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU	03/2018	1,016.92 -	1,071.00	-	- -	04/2021	-	0/0
130	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA	03/2018	806.11 -	806.11	21.39	- -	04/2021	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (January 2020)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
131	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH	03/2018	478.74 -	478.74	55.06	- -	05/2021	-	0/0
132	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	686.65	114.36	- 07/2020	06/2021	11(R3)	0/0
133	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	417.51	44.14	- -	06/2021	-	0/0
134	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	953.09	224.11	- 05/2020	06/2021	13(R3)	0/0
135	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	668.86	175.29	- 05/2020	06/2021	13(R3)	0/0
136	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	686.65	105.69	- 03/2020	06/2021	15(R3)	0/0
137	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	1,522.00	243.52	- 06/2021	06/2021	0(R3)	0/0
138	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	999.00	-	- -	06/2021	-	0/0
139	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	503.88	8.84	- -	06/2021	-	0/0
140	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA	11/2016	1,071.61 -	1,048.10	514.46	- -	07/2021	-	2/4
141	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA	11/2016	1,064.88 -	1,021.00	124.00	- -	07/2021	-	0/4
142	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	1,323.15	403.93	- -	07/2021	-	0/0
143	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI,WEST BENGAL	03/2018	1,261.98 -	1,261.98	793.49	- -	07/2021	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (January 2020)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
144	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 -	1,959.00	706.39	- -	07/2021	-	0/0
145	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 1,730.07	1,550.98	786.78	- -	07/2021	-	0/0
146	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64 1,687.00	1,437.64	564.11	- 12/2018	07/2021	31(R3)	0/0
147	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA	03/2018	634.70 931.21	931.21	143.54	- -	07/2021	-	0/0
148	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA	03/2018	795.50 -	799.30	128.56	- -	07/2021	-	0/0
149	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 -	1,162.92	15.36	- -	07/2021	-	0/0
150	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA	01/2018	607.00 512.99	607.00	187.53	- 02/2019	08/2021	30(R3)	0/1
151	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	614.48	93.00	- -	08/2021	-	0/0
152	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	564.66	89.77	- -	08/2021	-	0/0
153	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 2,190.00	2,400.00	1,740.36	- 05/2019	11/2021	30(R3)	0/0
154	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	1,117.84	-	- -	12/2021	-	0/0
155	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT	03/2018	1,161.39 1,404.00	1,161.39	-	- 11/2021	-	-	0/0
	Total		81,760.48 -	82,741.58	34,939.05				15/42
	URBAN DEVELOPMENT								

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (January 2020)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>Central Public Works Department</u>								
156	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00 -	422.00	15.11	- 03/2021	12/2020	-3(R3)	0/0
157	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 -	392.00	13.90	- 08/2020	03/2021	7(R3)	0/0
158	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU	11/2017	348.77 -	348.77	31.98	- -	11/2021	-	0/8
	Total		1,162.77 -	1,162.77	60.99				0/8
	Grand Total		1,11,356.96	1,29,476.64	51,725.80				40/118

Details of Projects Without Milestones w.r.t. Original Schedule

Annexure - X

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
	<u>Airport Authority Of India Limited</u>					
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,A & N ISLANDS	10/2013	314.61 -	09/2018 -	06/2020	0/0
2	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN - [N04000085]AAI,UTTARAKHAND	07/2018	353.27 -	09/2020 -	09/2020	0/0
3	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076]AAI,DELHI	11/2016	233.38 -	04/2020 -	12/2020	0/0
4	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA - [N04000080]AAI, WEST BENGAL	01/2016	219.91 -	03/2020 -	12/2020	0/0
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]AAI, ASSAM	12/2016	859.86 -	03/2021 -	03/2021	0/0
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT - [N04000079]AAI, MAHARASHTRA	03/2017	358.89 -	04/2021 -	04/2021	0/0
7	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]AAI, UTTAR PRADESH	06/2018	1,383.00 -	09/2021 -	09/2021	0/0
8	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]AAI, JAMMU AND KASHMIR	07/2018	323.19 -	09/2021 -	09/2021	0/0
9	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]AAI, TAMIL NADU	08/2018	951.28 -	10/2021 -	10/2021	0/0
10	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA - [N04000081]AAI, WEST BENGAL	01/2019	264.99 -	11/2021 -	11/2021	0/0
11	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI - [N04000074]AAI, TAMIL NADU	06/2018	2,467.00 -	02/2022 -	08/2022	0/0
12	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082]AAI, BIHAR	05/2018	539.20 -	10/2022 -	10/2022	0/0
13	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI, TRIPURA	09/2015	338.93 -	06/2019 -	-	0/0
	<u>COAL</u>					
	<u>Neyveli Lignite Corporation</u>					
14	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC, UTTAR PRADESH	07/2016	17,237.00 -	11/2021 -	11/2021	0/0
15	HADLA LIGNITE MINE PROJECT (1.90 MTPA) - [N06000144]NLC, RAJASTHAN	03/2015	522.45 -	09/2019 -	-	0/0
16	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC, RAJASTHAN	03/2015	513.63 -	12/2019 -	-	0/0
	<u>Western Coal Fields Limited</u>					
17	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL, MAHARASHTRA	03/2017	362.73 -	03/2020 -	03/2020	0/0
18	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL, MADHYA PRADESH	07/2016	409.87 -	03/2022 -	03/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	<u>PETROLEUM</u>					
	<u>Bharat Petroleum Corporation Limited</u>					
19	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00	02/2017	10/2021	0/0
20	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA	12/2015	1,112.00 1,507.24	06/2019 02/2022	02/2022	0/0
21	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]BPCL,JHARKHAND	11/2018	248.55	06/2022	06/2022	0/0
22	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]BPCL,KERALA	09/2018	11,130.00	03/2023	03/2023	0/0
	<u>Chennai Petroleum Corporation Limited</u>					
23	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU	09/2017	1,858.00	12/2019	04/2020	0/0
24	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU	08/2017	421.00	08/2020	02/2021	0/0
	<u>Gas Authority Of India Limited</u>					
25	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA	02/2015	749.00	02/2020	02/2020	0/0
	<u>Hindustan Petroleum Corporation Limited</u>					
26	SWRO II WITH LLPH FACILITIES - [N16000378]HPCL,ANDHRA PRADESH	09/2019	196.26	07/2020	07/2020	0/0
	<u>Indian Oil Corporation Limited</u>					
27	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00	06/2020	06/2020	0/0
28	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]IOCL,ANDHRA PRADESH	08/2017	384.58	04/2021	09/2020	0/0
29	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]IOCL,MADHYA PRADESH	08/2017	236.00	06/2020	10/2020	0/0
30	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL,WEST BENGAL	04/2016	1,021.00	12/2020	12/2020	0/0
31	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL,MAHARASHTRA	05/2016	261.00	01/2021	01/2021	0/0
32	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL,ANDHRA PRADESH	01/2015	342.00	03/2021	03/2021	0/0
33	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL,ANDHRA PRADESH	07/2014	247.00	03/2021	03/2021	0/0
34	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]IOCL,BIHAR	04/2018	522.00	03/2021	03/2021	0/0
35	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00	01/2021	04/2021	0/0
36	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH	08/2018	466.00	04/2021	07/2021	0/0
37	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383]IOCL,HARYANA	09/2019	164.69	07/2021	07/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
38	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	10/2020 -	08/2021	0/0
39	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]IOCL,HARYANA	01/2019	909.00 -	01/2021 -	08/2021	0/0
40	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]IOCL,ODISHA	11/2018	462.30 -	09/2021 -	09/2021	0/0
41	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 -	01/2021 -	10/2021	0/0
42	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]IOCL,ANDHRA PRADESH	10/2018	316.20 -	10/2021 -	10/2021	0/0
43	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]IOCL,HARYANA	08/2019	1,255.00 -	10/2021 -	10/2021	0/0
44	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	08/2021 -	11/2021	0/0
45	LAB REVAMP AT GUJARAT REFINERY - [N16000377]IOCL,GUJARAT	10/2019	403.00 -	12/2021 -	12/2021	0/0
46	LPG BP PROJECT CHITTOOR - [N16000381]IOCL,ANDHRA PRADESH	07/2019	167.00 -	07/2022 -	07/2022	0/0
47	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]IOCL,ODISHA	06/2019	371.00 -	09/2022 -	09/2022	0/0
48	R and D CAMPUS II AT FARIDABAD - [N16000375]IOCL,HARYANA	06/2019	2,281.94 -	12/2022 -	12/2022	0/0
49	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	04/2022 -	02/2023	0/0
50	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA	12/2018	611.00 -	04/2022 -	03/2023	0/0
51	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY - [N16000382]IOCL,GUJARAT	11/2019	5,251.00 -	05/2023 -	05/2023	0/0
<u>Indian Strategic Petroleum Reserves Ltd</u>						
52	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KARNATAKA	01/2006	993.00 -	01/2012 -	-	0/0
<u>Numaligarh Refinery Limited</u>						
53	NUMALIGARH REFINERY EXPANSION PROJECT - [N16000379]NRL,ASSAM	01/2019	22,594.00 -	10/2024 -	10/2024	0/0
<u>Oil India Limited</u>						
54	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN - [N16000356]OIL,ASSAM	06/2016	224.75 -	08/2020 -	08/2020	0/0
55	50MW WIND ENERGY POWER PROJECT - [N16000298]OIL,MULTI STATE	11/2015	500.00 -	06/2017 -	-	0/0
56	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM	07/2011	350.00 -	01/2019 -	-	0/0
<u>POWER</u>						
<u>National Hydro-Electric Power Corporation</u>						
57	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 08/2023	08/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
58	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR	12/1999	578.62 -	06/2006 -	-	0/0
	<u>National Thermal Power Corporation</u>					
59	TALAI PALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH	09/2015	3,004.00 -	11/2019 -	11/2019	0/0
60	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC,ODISHA	05/2016	1,885.13 -	12/2018 -	08/2020	0/0
61	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC,WEST BENGAL	12/2016	529.68 -	11/2018 -	08/2020	0/0
62	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000273]NTPC,UTTAR PRADESH	12/2018	587.44 -	09/2020 -	09/2020	0/0
63	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000274]NTPC,UTTAR PRADESH	03/2019	349.00 -	11/2020 -	11/2020	0/0
64	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,238.00	10/2017 -	-	0/0
	<u>Power Grid Corporation Of India Limited</u>					
65	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE	03/2017	283.72 -	11/2019 -	11/2019	0/0
66	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL, WEST BENGAL	04/2016	454.11 -	04/2018 01/2020	01/2020	0/0
67	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL, MULTI STATE	10/2016	608.24 -	04/2019 -	01/2020	0/0
68	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL, MULTI STATE	12/2015	3,654.00 -	04/2019 -	01/2020	0/0
69	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL, MULTI STATE	05/2016	3,519.59 -	05/2019 -	02/2020	0/0
70	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL, MULTI STATE	09/2017	198.49 -	09/2019 02/2020	02/2020	0/0
71	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL, MULTI STATE	01/2014	374.63 374.63	04/2016 12/2017	03/2020	0/0
72	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL, MULTI STATE	03/2015	197.40 197.40	03/2018 -	03/2020	0/0
73	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL, MULTI STATE	03/2016	808.63 -	01/2018 03/2020	03/2020	0/0
74	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL, MULTI STATE	05/2016	14,733.37 -	11/2019 -	03/2020	0/0
75	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL, MULTI STATE	10/2016	408.46 -	01/2019 09/2019	03/2020	0/0
76	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL, MULTI STATE	02/2017	322.30 -	02/2019 04/2020	03/2020	0/0
77	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL, MULTI STATE	02/2017	235.53 -	06/2019 -	03/2020	0/0
78	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL, MULTI STATE	03/2017	379.95 -	12/2019 -	03/2020	0/0
79	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL, GUJARAT	05/2017	175.64 -	09/2018 03/2020	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
80	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 -	07/2019 -	03/2020	0/0
81	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT	12/2017	193.14 -	06/2019 03/2020	03/2020	0/0
82	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL,MULTI STATE	02/2017	5,070.13 -	04/2020 -	04/2020	0/0
83	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA	05/2017	445.89 -	02/2019 12/2019	05/2020	0/0
84	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE	11/2017	358.83 -	05/2020 -	05/2020	0/0
85	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALAR EN - [N18000264]PGCIL,MULTI STATE	08/2017	1,931.39 -	02/2020 -	06/2020	0/0
86	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE	03/2017	3,500.00 3,500.00	07/2020 -	07/2020	0/0
87	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	12/2018 -	12/2020	0/0
88	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	12/2018 -	12/2020	0/0
	<u>Thdc India Limited</u>					
89	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH	03/2019	11,089.42 -	09/2023 -	09/2023	0/0
	<u>HEAVY INDUSTRY</u>					
	<u>Bharat Heavy Electricals Limited</u>					
90	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL,DELHI	08/2016	1,554.00 -	09/2019 -	03/2020	0/0
	<u>HEALTH AND FAMILY WELFARE</u>					
	<u>Central Public Works Department</u>					
91	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR - [N21000029]CPWD,JAMMU AND KASHMIR	03/2019	1,404.00 -	09/2023 -	09/2023	0/0
92	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]CPWD,JAMMU AND KASHMIR	03/2019	1,577.00 -	09/2025 -	09/2025	0/0
	<u>Hill Infra Tech Services Limited</u>					
93	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	04/2020 -	10/2020	0/0
94	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	06/2020 -	10/2020	0/0
95	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 -	05/2021 08/2021	10/2021	0/0
	<u>Hospital Services Consultancy Corporation Ltd</u>					
96	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL	08/2016	244.00 -	09/2018 -	05/2019	0/0
97	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	03/2019 -	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
98	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	03/2019 -	03/2020	0/0
99	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH	03/2018	268.84 -	- -	04/2020	0/0
100	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI	12/2017	156.56 -	- -	05/2020	0/0
101	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA	01/2018	249.01 -	- -	05/2020	0/0
102	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA	03/2018	582.99 -	- -	06/2020	0/0
103	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	05/2018 -	07/2020	0/0
104	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL	08/2017	355.15 -	03/2019 -	07/2020	0/0
105	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH	03/2018	601.02 -	- -	07/2020	0/0
106	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC,WEST BENGAL	04/2018	651.99 -	- -	07/2020	0/0
107	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	09/2020	0/0
	<u>National Building Construcion Corporation Ltd</u>					
108	AIIMS BILASPUR - [N21000028]NBCC,HIMACHAL PRADESH	04/2018	1,351.00 1,471.00	09/2021 -	09/2021	0/0
	<u>RAILWAYS</u>					
	<u>Central Railways</u>					
109	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 199.12	03/2019 03/2020	03/2020	0/0
110	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50 -	03/2021 -	03/2022	0/0
111	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89 -	03/2021 -	03/2022	0/0
112	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	3,168.29 -	03/2023 -	03/2023	0/0
113	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19 -	03/2022 -	03/2023	0/0
114	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,449.91 -	03/2023 -	03/2023	0/0
115	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA	02/2015	3,627.47 3,627.00	03/2024 -	03/2023	0/0
116	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA	02/2016	1,876.00 -	03/2023 -	03/2023	0/0
117	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02 -	03/2022 -	03/2024	0/0
118	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA	02/2016	9,968.00 -	03/2024 -	03/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
119	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA	02/2016	2,425.00	03/2024	03/2024	0/0
120	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16	03/2022	03/2024	0/0
121	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95	03/2023	03/2024	0/0
122	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00	03/2024	-	0/0
	<u>Container Corporation Of India</u>					
123	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00	03/2019	12/2019	0/0
124	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00	03/2019	02/2020	0/0
125	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17	03/2018	03/2020	0/0
126	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32	03/2019	03/2020	0/0
127	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50	03/2019	12/2020	0/0
128	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH	01/2013	387.70	03/2018	-	0/0
129	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH	05/2014	207.00	03/2018	-	0/0
130	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00	03/2019	-	0/0
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>					
131	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE	11/2007	16,592.00 51,101.00	03/2020	03/2020	0/0
132	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	11,589.00 30,357.00	-	-	0/0
	<u>East Central Railways</u>					
133	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR,BIHAR	04/1998	180.82 726.31	-	10/2019	0/0
134	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	324.73 898.53	03/2012	03/2020	0/0
135	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	499.41 516.02	03/2020	03/2020	0/0
136	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	477.88 751.55	03/2012	03/2020	0/0
137	GARHWA ROAD-RAMNA - [N22000465]ECR,JHARKHAND	03/2015	348.23	03/2021	12/2020	0/0
138	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	1,033.07 3,020.95	-	03/2021	0/0
139	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 1,625.87	-	03/2021	0/0
140	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR	04/1999	325.00 735.20	-	03/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
141	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 1,470.50	- -	03/2021	0/0
142	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	03/2020 -	03/2021	0/0
143	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	03/2019 -	03/2021	0/0
144	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]ECR,BIHAR	04/1991	329.39 803.11	- -	12/2021	0/0
145	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 614.45	- -	03/2022	0/0
146	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR	04/2006	378.56 -	- -	03/2022	0/0
147	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	548.00 819.01	03/2020 -	03/2022	0/0
148	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 1,215.54	03/2021 -	03/2022	0/0
149	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 1,185.73	03/2021 -	03/2022	0/0
150	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 519.33	- -	02/2023	0/0
151	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 2,066.78	- -	03/2023	0/0
152	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	1,605.17 1,605.17	- 03/2023	03/2023	0/0
153	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR	04/2008	326.20 -	- -	03/2024	0/0
154	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	03/2024	0/0
155	DANIYAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-	0/0
156	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 546.71	07/2014 -	-	0/0
157	ARA-BHABHUA ROAD (NL) - [N22000166]ECR,BIHAR	04/2008	633.87 -	- -	-	0/0
158	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-	0/0
159	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR	04/2008	445.25 -	- -	-	0/0
160	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE	04/2008	415.67 -	- -	-	0/0
161	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-	0/0
162	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-	0/0
163	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-	0/0
164	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
165	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-	0/0
	<u>East Coast Railway</u>					
166	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	03/2020 -	03/2021	0/0
167	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 1,539.28	02/2019 03/2022	03/2022	0/0
168	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 701.61	11/2018 -	03/2022	0/0
169	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 843.04	10/2020 03/2023	03/2023	0/0
170	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 1,547.38	03/2022 03/2023	03/2023	0/0
171	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 1,172.92	12/2018 03/2022	03/2023	0/0
172	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 2,499.71	03/2022 03/2024	03/2024	0/0
173	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 3,791.66	03/2009 -	06/2024	0/0
174	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 198.07	06/2021 -	06/2024	0/0
175	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 2,361.74	03/2022 -	03/2025	0/0
	<u>Eastern Railways</u>					
176	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	05/2019	0/0
177	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	03/2020	0/0
178	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	11/2018 -	03/2021	0/0
179	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	542.18 -	03/2020 -	03/2021	0/0
180	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	03/2021	0/0
181	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	09/2021	0/0
182	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	02/2013 -	03/2024	0/0
183	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	03/2024	0/0
184	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	03/2019 12/2009	03/2025	0/0
185	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	03/2006 -	03/2025	0/0
186	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	03/2025	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
187	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	03/2025	0/0
188	PIRPAINI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	03/2022 -	03/2025	0/0
189	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	03/2016 -	03/2025	0/0
190	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.51 -	03/2017 -	03/2025	0/0
191	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	03/2025	0/0
192	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	03/2016 -	03/2025	0/0
193	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	03/2017 -	03/2025	0/0
194	BARIARPIUR-MANANPUR VIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	03/2025	0/0
195	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	03/2025	0/0
196	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	03/2005 -	03/2025	0/0
197	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	03/2025	0/0
198	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	03/2025	0/0
199	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96 -	02/2012 -	03/2025	0/0
200	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2025	0/0
201	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGREGATION OF ARRIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	03/2025	0/0
202	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	03/2017 -	03/2026	0/0
<u>Indian Railway Construction Company Limited</u>						
203	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA	04/2016	5,200.00 -	03/2020 -	06/2023	0/0
<u>Kolkata Metro Rail Corporation Limited</u>						
204	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-	0/0
<u>Metropolitan Rapid Transport Projects</u>						
205	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 1,781.98	03/2004 -	03/2021	0/0
206	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 -	03/2014 -	03/2021	0/0
207	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	06/2021	0/0
208	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	03/2025	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
209	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-	0/0
210	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	-	0/0
	<u>North Central Railway</u>					
211	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR, UTTAR PRADESH	03/2018	4,329.53 -	03/2023 -	03/2023	0/0
212	ETAWAH-MAINPURI (NL), NCR - [220100318]NCR, UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-	0/0
213	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR, MULTI STATE	04/2010	2,030.50 -	- -	-	0/0
	<u>North East Frontier Railway</u>					
214	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR - [220100135]NFR, WEST BENGAL	04/1983	297.32 -	03/2019 -	03/2020	0/0
215	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	385.20 1,532.00	03/2019 -	03/2020	0/0
216	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR, BIHAR	09/2006	532.87 2,145.00	03/2019 -	03/2020	0/0
217	DIMAPUR-TIZIT NL - [N22000196]NFR, NAGALAND	04/2013	4,274.00 -	03/2020 -	03/2020	0/0
218	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR, MULTI STATE	04/2010	242.22 -	03/2020 -	03/2020	0/0
219	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR, MULTI STATE	04/2011	414.84 -	03/2020 -	03/2020	0/0
220	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR, ASSAM	04/2011	314.00 728.00	03/2019 -	03/2020	0/0
221	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR, ASSAM	04/2015	2,232.32 -	03/2022 -	03/2020	0/0
222	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR, WEST BENGAL	04/2016	602.27 -	12/2021 -	03/2020	0/0
223	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	1,180.19 3,300.00	12/2008 -	03/2021	0/0
224	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR, MEGHALAYA	04/2010	906.46 -	03/2021 -	03/2021	0/0
225	DIGARU-HOJAI (102 KM) - [N22000389]NFR, ASSAM	04/2015	870.96 -	03/2021 -	03/2021	0/0
226	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR, MULTI STATE	04/2010	241.52 -	- -	06/2021	0/0
227	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND	04/2006	2,326.52 -	03/2015 -	10/2021	0/0
228	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR	04/2003	4,454.17 13,809.00	03/2011 -	03/2022	0/0
229	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	2,393.47 4,968.00	03/2014 03/2022	03/2022	0/0
230	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR, BIHAR	04/2008	333.76 -	- 03/2022	03/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
231	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42	-	03/2022	0/0
232	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48	12/2015	-	0/0
233	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR, MULTI STATE	04/2013	1,798.00	03/2019	-	0/0
234	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR, MULTI STATE	04/1999	819.23	-	-	0/0
235	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHOWA-JAIN - [N22000499]NFR, WEST BENGAL	02/1999	380.60	04/2010	-	0/0
<u>North Eastern Railway</u>						
236	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER, UTTAR PRADESH	03/2015	1,295.42	03/2022	12/2019	0/0
237	CHHAPRA-BALLIA UP - [N22000134]NER, MULTI STATE	03/2013	295.00	01/2019	01/2020	0/0
238	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER, UTTAR PRADESH	04/2017	622.50	04/2017	01/2020	0/0
239	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER, UTTAR PRADESH	04/2016	213.00	04/2016	06/2020	0/0
240	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER, UTTAR PRADESH	04/2016	1,177.96	12/2019	04/2021	0/0
241	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER, MULTI STATE	03/2007	243.78	12/2021	12/2021	0/0
242	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER, UTTAR PRADESH	04/2016	1,900.00	01/2022	01/2022	0/0
243	AUNRIHAR - JAUNPUR PATCH DOUBLING. - [N22000469]NER, UTTAR PRADESH	04/2016	600.00	01/2022	01/2022	0/0
244	ETAH - KASGANJ - NEW LINE - [N22000462]NER, UTTAR PRADESH	04/2017	276.90	04/2017	04/2022	0/0
245	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER, UTTAR PRADESH	04/2017	150.00	04/2017	10/2022	0/0
246	HATHUA-BHATNI (N L) (NER) - [220100319]NER, MULTI STATE	04/2005	230.03	12/2022	12/2022	0/0
247	KICHHA-KHATIMA (NL) - NER - [220100317]NER, UTTARAKHAND	04/2003	142.45	-	-	0/0
248	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER, UTTAR PRADESH	03/2013	307.00	-	-	0/0
249	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER, UTTAR PRADESH	03/2013	643.00	-	-	0/0
250	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER, UTTAR PRADESH	04/2014	182.92	-	-	0/0
251	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER, UTTAR PRADESH	04/2017	1,343.00	01/2018	-	0/0
252	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER, UTTAR PRADESH	04/2016	602.50	-	-	0/0
<u>North Western Railway</u>						

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
253	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	10/2018 -	12/2019	0/0
254	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 281.03	02/2019 -	02/2020	0/0
255	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	420.18 -	03/2020 -	12/2020	0/0
256	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	11/2019 -	12/2020	0/0
257	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	12/2019 -	02/2021	0/0
258	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 780.98	02/2019 -	06/2021	0/0
259	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	03/2020 -	04/2022	0/0
260	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	08/2022 -	09/2022	0/0
261	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0
262	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-	0/0
<u>Northern Railway</u>						
263	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	06/2020	0/0
264	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 695.00	12/2011 -	03/2021	0/0
265	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 -	03/2016 -	03/2021	0/0
266	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	03/2022	0/0
267	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	11/2002 -	06/2022	0/0
268	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	03/2023	0/0
269	UNCHAHAH-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	1,229.00 -	- -	03/2023	0/0
270	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE	04/2007	328.14 -	03/2023 -	03/2023	0/0
271	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 2,010.00	07/2012 -	03/2024	0/0
272	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	03/2024	0/0
273	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	03/2024	0/0
<u>National High Speed Rail Corporation Limited</u>						
274	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE	12/2015	1,08,000.00 -	12/2023 12/2023	12/2023	0/0
<u>Rail India Technical And Economic Service</u>						

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
275	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-	0/0
	<u>Rail Vikas Nigam Ltd.</u>					
276	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	1,185.64 -	12/2017 -	03/2020	0/0
277	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	03/2019 -	03/2020	0/0
278	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	03/2016 -	12/2020	0/0
279	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	1,402.02 -	03/2020 -	12/2020	0/0
280	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT	04/2012	644.38 -	03/2021 -	03/2021	0/0
281	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	713.48 -	03/2020 -	03/2021	0/0
282	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	948.04 -	03/2020 -	03/2021	0/0
283	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH	04/2011	1,485.85 -	12/2020 -	03/2021	0/0
284	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70 -	02/2015 -	12/2021	0/0
285	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT	04/2012	975.62 -	12/2021 -	12/2021	0/0
286	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,548.66 -	12/2021 -	03/2022	0/0
287	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	03/2020 -	03/2022	0/0
288	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	03/2019 -	06/2022	0/0
289	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	12/2020 -	12/2022	0/0
290	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH	04/2015	3,246.26 -	12/2023 -	12/2023	0/0
291	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60 -	03/2022 -	12/2024	0/0
292	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA	04/2015	773.94 -	12/2024 -	12/2024	0/0
293	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92 -	03/2023 -	12/2024	0/0
294	VIZIANAGARAM - SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA	01/1991	2,335.67 -	12/2024 -	12/2024	0/0
295	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	03/2016 -	03/2025	0/0
296	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	03/2016 -	03/2025	0/0
297	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00 -	12/2024 -	03/2025	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
298	DIGHI PORT NEW LINE - [N22000408]RVNL, MAHARASHTRA	04/2015	723.78 -	12/2025 -	03/2025	0/0
299	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	12/2025	0/0
300	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL, HIMACHAL PRADESH	04/2008	2,966.99 -	12/2026 -	12/2025	0/0
	<u>Railway Electrification</u>					
301	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE, UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-	0/0
	<u>South Central Railway</u>					
302	MUNEERABAD-MAHABOONNAGAR(NL), SCR - [220100205]SCR, MULTI STATE	04/1997	1,723.00 1,780.29	03/2000 -	03/2021	0/0
303	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR, TELANGANA	04/2017	119.73 176.17	03/2022 -	12/2022	0/0
304	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR, ANDHRA PRADESH	12/2001	1,045.20 2,120.16	03/2009 -	03/2023	0/0
305	KAZIPET-BALHARSHA - [N22000367]SCR, MULTI STATE	04/2015	2,063.03 2,063.03	03/2021 -	03/2023	0/0
306	GUNTUR-GUNTAKAL - [N22000368]SCR, ANDHRA PRADESH	04/2016	3,631.00 3,631.00	03/2022 -	03/2023	0/0
307	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR, MULTI STATE	04/2012	1,856.95 1,952.68	03/2023 -	03/2024	0/0
308	NANDYAL-YERRAGUNTALA(NL), SCR - [220100192]SCR, ANDHRA PRADESH	03/1996	164.36 -	02/2009 -	-	0/0
309	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR, TELANGANA	07/1998	458.25 458.25	- -	-	0/0
310	GUDUR-DURGARAJPATNAM - [N22000265]SCR, ANDHRA PRADESH	04/2011	761.37 761.37	- -	-	0/0
311	DUVVADA-VIJAYAWADA - [N22000366]SCR, ANDHRA PRADESH	04/2015	3,873.07 3,873.07	- -	-	0/0
	<u>South East Central Railway</u>					
312	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, MADHYA PRADESH	04/2005	383.79 1,473.76	- 01/2020	01/2020	0/0
313	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR, CHHATISGARH	04/2008	872.00 1,226.51	12/2019 03/2020	03/2020	0/0
314	ANUPPUR-KATNI - [N22000485]SECR, MADHYA PRADESH	04/2015	1,370.00 1,370.94	12/2021 03/2023	03/2023	0/0
	<u>South Eastern Railway</u>					
315	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER, JHARKHAND	04/2012	148.77 -	12/2016 08/2018	03/2020	0/0
316	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER, JHARKHAND	04/2012	258.20 358.68	12/2018 12/2018	08/2020	0/0
317	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER, ODISHA	11/2015	969.83 1,312.96	03/2020 03/2020	03/2021	0/0
318	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER, JHARKHAND	03/2016	1,724.20 -	03/2021 03/2021	12/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
319	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	- 03/2025	03/2025	0/0
320	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER, MULTI STATE	04/2010	651.00 -	03/2015 03/2025	03/2025	0/0
321	BANKURA - DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER, WEST BENGAL	04/1998	1,027.40 1,966.70	03/2003 03/2030	03/2030	0/0
322	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER, ODISHA	04/2010	149.90 -	03/2015 -	-	0/0
323	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-	0/0
<u>South Western Railway</u>						
324	YELAHANKA-PENKONDA - [N22000328]SWR, MULTI STATE	05/2015	860.43 -	03/2020 -	03/2020	0/0
325	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR, KARNATAKA	03/1996	644.78 644.78	03/2017 -	03/2020	0/0
326	HOTGI-KUDGI-GADAG - [N22000333]SWR, MULTI STATE	03/2015	1,614.59 1,870.41	03/2019 -	03/2021	0/0
327	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR, KARNATAKA	04/2011	1,801.01 1,801.01	- -	12/2023	0/0
328	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR, KARNATAKA	04/2013	558.00 692.43	- -	12/2023	0/0
329	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR, MULTI STATE	04/2013	296.00 466.65	- -	12/2023	0/0
330	WHITE FIELD-KOLAR NL - [N22000280]SWR, KARNATAKA	04/2011	348.85 348.85	- -	12/2023	0/0
331	TORANAGALLU-RANJITPURA DL - [N22000298]SWR, KARNATAKA	04/2011	146.75 146.75	- -	12/2023	0/0
332	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR, KARNATAKA	04/2013	327.25 367.77	- -	12/2023	0/0
333	MARIKUPPAM - KUPPAM - [N22000308]SWR, KARNATAKA	04/2012	279.54 279.54	03/2016 -	12/2023	0/0
334	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR, KARNATAKA	04/1996	1,382.78 1,382.78	03/2002 -	03/2024	0/0
335	SHIMOGA-HARIHAR NL - [N22000278]SWR, KARNATAKA	04/2011	832.47 832.47	03/2016 -	03/2024	0/0
336	HUBLI-ANKOLA(NL), SWR - [220100193]SWR, KARNATAKA	04/1997	2,315.00 -	- -	12/2024	0/0
337	GADAG-WADI NL - [N22000299]SWR, KARNATAKA	04/2013	2,841.84 2,841.84	12/2018 -	12/2024	0/0
<u>Southern Railway</u>						
338	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR, MULTI STATE	04/2011	120.70 -	03/2019 -	12/2019	0/0
339	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY'-AGASTIYAMPALLI - [N22000079]SR, TAMIL NADU	09/2007	724.69 -	02/2019 -	02/2020	0/0
340	MADURAI-BODINAYAKKANUR - [N22000201]SR, TAMIL NADU	04/2008	164.41 -	- -	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
341	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	931.98 -	- -	03/2020	0/0
342	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU	10/2013	187.26 -	04/2014 -	03/2020	0/0
343	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	03/2020 -	03/2021	0/0
344	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU	02/2015	760.00 -	03/2020 -	06/2021	0/0
345	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU	02/2015	1,700.00 -	03/2022 -	03/2022	0/0
346	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	03/2024 -	03/2026	0/0
347	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	1,566.00 -	- -	-	0/0
348	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	227.40 -	- -	-	0/0
349	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	- -	-	0/0
350	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	151.84 -	02/2019 -	-	0/0
351	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-	0/0
352	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-	0/0
353	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-	0/0
354	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-	0/0
355	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-	0/0
356	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-	0/0
357	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-	0/0
358	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 -	- -	-	0/0
359	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	- -	-	0/0
360	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	03/2005 -	-	0/0
361	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-	0/0
362	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU	02/1999	257.00 257.00	03/2018 -	-	0/0
<u>Western Railway</u>						
363	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	03/2017	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
364	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT	02/1991	551.51 809.07	03/2019 03/2020	03/2020	0/0
365	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	829.74 1,215.34	03/2020 03/2021	03/2021	0/0
366	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	844.10 844.10	- 03/2021	03/2021	0/0
367	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 1,002.39	03/2021 03/2021	03/2021	0/0
368	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT	04/2017	691.84 663.29	03/2020 03/2021	03/2021	0/0
369	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH	04/2016	700.00 603.69	06/2020 06/2021	06/2021	0/0
370	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 321.62	03/2012 03/2022	03/2022	0/0
371	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 1,347.26	03/2022 03/2022	03/2022	0/0
372	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 858.56	03/2019 03/2022	03/2022	0/0
373	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	1,037.15 1,037.15	03/2021 03/2022	03/2022	0/0
374	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	3,503.69 3,975.22	03/2022 03/2023	03/2023	0/0
375	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 1,640.04	03/2022 03/2023	03/2023	0/0
376	GANDHINAGAR REDEVELOPMENT OF STATION ALONG WITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATION - [N22000433]WR,GUJARAT	03/2017	243.60 -	- -	-	0/0
377	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-	0/0
378	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-	0/0
379	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-	0/0
380	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 -	- -	-	0/0
	ROAD TRANSPORT AND HIGHWAYS					
	Ministry Of Road Transport And Highways (State Pwds)					
381	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	12/2019	0/0
382	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA	03/2018	256.15 -	12/2019 -	12/2019	0/0
383	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O - [N24000871]MoRTH,WEST BENGAL	08/2014	600.87 720.97	11/2017 05/2019	05/2019	0/0
384	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873]MoRTH,WEST BENGAL	08/2014	823.20 937.76	11/2017 06/2019	06/2019	0/0
385	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]MoRTH,WEST BENGAL	04/2014	279.70 398.52	08/2017 07/2019	07/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
386	MAJALGAON TO KAIJ - [N24001036]MoRTH,MAHARASHTRA	01/2017	413.99 -	07/2019 -	07/2019	0/0
387	REHABILITATION AND UPGADATION OF ALLAHABAD -MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2- - [N24001147]MoRTH,UTTAR PRADESH	10/2016	239.63 -	02/2019 -	07/2019	0/0
388	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 - [N24000962]MoRTH,MADHYA PRADESH	09/2016	178.23 -	09/2018 -	08/2019	0/0
389	REHABILITATION AND UPGADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO - [N24001143]MoRTH,UTTAR PRADESH	10/2016	176.94 177.00	10/2018 -	09/2019	0/0
390	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH	01/2012	410.72 -	04/2015 -	10/2019	0/0
391	REHABILITATION AND UPGADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]MoRTH,UTTAR PRADESH	11/2016	215.16 215.00	09/2019 -	10/2019	0/0
392	REHABILITATION AND UPGADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]MoRTH,UTTAR PRADESH	10/2013	445.89 653.00	03/2017 -	10/2019	0/0
393	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]MoRTH,WEST BENGAL	03/2016	271.17 291.20	11/2018 11/2019	11/2019	0/0
394	BHADGAON TO CHALISGAON - [N24001047]MoRTH,MAHARASHTRA	01/2018	259.55 260.00	11/2019 -	11/2019	0/0
395	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]MoRTH,ARUNACHAL PRADESH	03/2012	207.03 389.45	05/2012 05/2015	12/2019	0/0
396	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]MoRTH,SIKKIM	04/2013	151.59 240.58	08/2013 -	12/2019	0/0
397	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]MoRTH,SIKKIM	01/2013	182.28 -	02/2013 -	12/2019	0/0
398	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA	02/2017	203.21 203.00	05/2019 -	12/2019	0/0
399	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA	01/2017	385.87 386.00	06/2019 -	12/2019	0/0
400	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA	03/2018	249.29 -	12/2019 -	12/2019	0/0
401	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA	03/2018	219.91 -	12/2019 -	12/2019	0/0
402	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA	03/2018	228.31 -	12/2019 -	12/2019	0/0
403	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA	03/2018	223.46 -	12/2019 -	12/2019	0/0
404	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA	03/2018	177.84 177.00	12/2019 -	12/2019	0/0
405	REHABILITATION AND UPGADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]MoRTH,MAHARASHTRA	03/2016	536.65 356.00	12/2019 -	12/2019	0/0
406	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA	12/2017	309.94 310.00	12/2019 -	12/2019	0/0
407	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA	12/2017	244.04 244.00	03/2019 -	12/2019	0/0
408	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA	01/2018	264.41 264.00	03/2019 -	12/2019	0/0
409	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA	02/2018	355.99 355.99	12/2019 -	12/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
410	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM - [N24001153]MoRTH,ASSAM	11/2010	197.37 -	02/2014 -	12/2019	0/0
411	REHABILITATION AND UPGRADATION OF BARAICH -SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA - [N24001202]MoRTH,UTTAR PRADESH	03/2016	388.83 -	12/2019 -	12/2019	0/0
412	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148]MoRTH,UTTAR PRADESH	03/2016	599.34 -	01/2020 -	01/2020	0/0
413	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH,MADHYA PRADESH	03/2015	511.83 -	08/2017 -	02/2020	0/0
414	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MoRTH,UTTARAKHAND	02/2018	418.88 -	02/2020 -	02/2020	0/0
415	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]MoRTH,UTTAR PRADESH	03/2018	185.18 -	02/2020 -	02/2020	0/0
416	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH,MADHYA PRADESH	06/2015	390.51 -	- -	03/2020	0/0
417	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 - [N24000895]MoRTH,MADHYA PRADESH	09/2016	287.34 -	01/2019 -	03/2020	0/0
418	REHABILITATION AND UPGRADATION OF HARPALPUR -SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942]MoRTH,UTTAR PRADESH	03/2016	208.50 -	11/2019 -	03/2020	0/0
419	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA	10/2016	248.83 -	03/2019 -	03/2020	0/0
420	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH,TELANGANA	01/2017	300.00 -	05/2019 -	03/2020	0/0
421	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA - [N24001139]MoRTH,UTTAR PRADESH	10/2016	218.94 219.00	03/2020 -	03/2020	0/0
422	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH,UTTAR PRADESH	03/2016	240.30 240.00	01/2020 -	03/2020	0/0
423	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH - [N24001145]MoRTH,UTTAR PRADESH	05/2013	164.54 165.00	08/2015 -	03/2020	0/0
424	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]MoRTH,UTTAR PRADESH	03/2016	249.50 -	05/2019 -	03/2020	0/0
425	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203]MoRTH,UTTAR PRADESH	10/2016	218.90 -	03/2020 -	03/2020	0/0
426	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH	03/2018	233.04 -	03/2018 -	04/2020	0/0
427	UPGRADATION OF MAKSDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH	02/2018	279.44 -	03/2018 -	04/2020	0/0
428	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]MoRTH,TELANGANA	02/2018	426.52 -	04/2020 -	04/2020	0/0
429	R AND U FROM KM 385.00 TO KM 420.000 TO 2- LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404 - [N24001205]MoRTH,UTTAR PRADESH	12/2016	209.10 -	10/2019 04/2020	04/2020	0/0
430	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]MoRTH,UTTAR PRADESH	03/2018	263.89 242.05	04/2020 -	04/2020	0/0
431	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]MoRTH,MADHYA PRADESH	11/2013	497.05 -	05/2017 -	05/2020	0/0
432	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MoRTH,UTTARAKHAND	05/2018	248.00 -	05/2020 -	05/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
433	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH	03/2018	162.56 -	03/2018 -	05/2020	0/0
434	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]MoRTH,MADHYA PRADESH	11/2017	235.91 -	02/2018 -	05/2020	0/0
435	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]MoRTH,MADHYA PRADESH	11/2017	184.62 -	02/2018 -	05/2020	0/0
436	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884]MoRTH,MADHYA PRADESH	03/2018	191.21 -	11/2019 -	05/2020	0/0
437	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]MoRTH,TELANGANA	01/2018	283.15 -	05/2020 -	05/2020	0/0
438	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA	05/2018	171.60 -	05/2018 -	05/2020	0/0
439	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH	03/2018	166.21 -	08/2018 -	06/2020	0/0
440	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]MoRTH,MADHYA PRADESH	03/2018	217.22 226.88	08/2018 -	06/2020	0/0
441	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH	11/2017	249.05 -	07/2018 -	06/2020	0/0
442	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]MoRTH,HARYANA	01/2017	247.25 -	03/2019 06/2020	06/2020	0/0
443	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906]MoRTH,PUNJAB	03/2018	173.24 -	06/2020 -	06/2020	0/0
444	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA	10/2016	298.32 -	02/2019 -	06/2020	0/0
445	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]MoRTH,TELANGANA	02/2018	206.13 -	06/2020 -	06/2020	0/0
446	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA	01/2017	391.06 391.00	06/2019 -	06/2020	0/0
447	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSI PUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131]MoRTH,JHARKHAND	03/2018	212.99 -	06/2020 -	06/2020	0/0
448	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]MoRTH,MIZORAM	08/2010	186.96 -	09/2014 06/2020	06/2020	0/0
449	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]MoRTH,UTTAR PRADESH	07/2016	208.88 -	10/2019 -	06/2020	0/0
450	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH,MADHYA PRADESH	02/2018	169.63 -	03/2018 -	07/2020	0/0
451	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]MoRTH,MADHYA PRADESH	03/2016	877.79 -	06/2019 -	07/2020	0/0
452	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905]MoRTH,PUNJAB	03/2018	322.48 -	07/2020 -	07/2020	0/0
453	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]MoRTH,TELANGANA	03/2018	626.76 -	07/2020 -	07/2020	0/0
454	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]MoRTH,MADHYA PRADESH	12/2015	957.54 -	02/2020 -	08/2020	0/0
455	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]MoRTH,PUNJAB	03/2018	293.10 -	08/2020 -	08/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
456	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927]MoRTH,PUNJAB	03/2018	293.64 -	08/2020 -	08/2020	0/0
457	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]MoRTH,PUNJAB	03/2018	293.64 -	08/2020 -	08/2020	0/0
458	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA	09/2018	301.38 301.00	08/2020 -	08/2020	0/0
459	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]MoRTH,TRIPURA	10/2016	171.90 -	08/2020 -	08/2020	0/0
460	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208]MoRTH,UTTAR PRADESH	03/2018	288.30 -	08/2020 -	08/2020	0/0
461	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH	11/2015	628.45 -	01/2020 -	09/2020	0/0
462	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH	01/2017	205.05 -	03/2017 -	09/2020	0/0
463	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]MoRTH,MADHYA PRADESH	11/2017	254.17 -	02/2018 -	09/2020	0/0
464	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]MoRTH,MADHYA PRADESH	01/2017	373.82 -	09/2019 -	09/2020	0/0
465	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]MoRTH,MADHYA PRADESH	01/2016	809.16 -	07/2018 -	09/2020	0/0
466	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]MoRTH,TELANGANA	03/2018	322.81 -	09/2020 -	09/2020	0/0
467	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MoRTH,MADHYA PRADESH	11/2017	392.33 428.55	03/2018 -	09/2020	0/0
468	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH,ARUNACHAL PRADESH	11/2016	243.89 -	- -	09/2020	0/0
469	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]MoRTH,UTTAR PRADESH	03/2016	296.50 -	09/2020 -	09/2020	0/0
470	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883]MoRTH,WEST BENGAL	03/2018	254.30 254.30	10/2020 -	10/2020	0/0
471	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. - [N24001174]MoRTH,MANIPUR	10/2016	235.31 -	11/2020 -	11/2020	0/0
472	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]MoRTH,NAGALAND	03/2017	217.35 -	11/2020 -	11/2020	0/0
473	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]MoRTH,MIZORAM	11/2010	624.41 -	03/2011 12/2020	12/2020	0/0
474	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH	03/2018	214.69 -	03/2018 -	12/2020	0/0
475	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH,PUNJAB	10/2017	1,069.59 -	10/2019 12/2020	12/2020	0/0
476	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]MoRTH,BIHAR	05/2014	199.98 -	08/2016 -	12/2020	0/0
477	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]MoRTH,NAGALAND	10/2016	167.62 -	12/2020 -	12/2020	0/0
478	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]MoRTH,NAGALAND	10/2016	172.63 -	12/2020 -	12/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
479	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 KM - [N24001230]MoRTH,UTTAR PRADESH	11/2018	281.45 -	12/2020 -	12/2020	0/0
480	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]MoRTH,MADHYA PRADESH	01/2019	264.50 -	03/2021 -	03/2021	0/0
481	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH,PUNJAB	03/2018	170.57 192.48	11/2020 -	05/2021	0/0
482	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA	02/2017	157.32 188.00	05/2019 -	05/2021	0/0
483	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]MoRTH,MIZORAM	08/2010	193.69 -	10/2010 06/2021	06/2021	0/0
484	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197]MoRTH,GUJARAT	03/2018	351.00 -	06/2021 -	06/2021	0/0
485	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH,WEST BENGAL	03/2016	160.27 213.97	08/2019 -	08/2021	0/0
486	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH,WEST BENGAL	06/2016	236.78 263.26	08/2019 -	08/2021	0/0
487	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152]MoRTH,ASSAM	09/2018	160.00 -	09/2021 -	09/2021	0/0
488	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I - [N24001216]MoRTH,JHARKHAND	12/2016	196.00 -	09/2021 -	09/2021	0/0
489	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]MoRTH,MADHYA PRADESH	11/2011	954.43 1,191.51	09/2015 -	10/2021	0/0
490	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180]MoRTH,NAGALAND	03/2019	237.51 -	12/2022 -	12/2022	0/0
491	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA	03/2015	153.21 -	01/2017 -	-	0/0
492	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]MoRTH,KERALA	01/2014	255.75 348.00	09/2017 -	-	0/0
493	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MoRTH,MAHARASHTRA	10/2015	289.60 -	- -	-	0/0
494	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MoRTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-	0/0
495	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]MoRTH,CHHATISGARH	12/2015	291.05 -	- -	-	0/0
496	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]MoRTH,CHHATISGARH	11/2015	485.44 -	12/2015 -	-	0/0
497	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MoRTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-	0/0
498	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MoRTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-	0/0
499	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MoRTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-	0/0
500	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MoRTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-	0/0
501	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MoRTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
502	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]MoRTH,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-	0/0
503	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]MoRTH,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-	0/0
504	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]MoRTH,SIKKIM	04/2013	166.27 -	08/2013 -	-	0/0
505	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]MoRTH,NAGALAND	12/2010	1,296.00 -	02/2011 -	-	0/0
506	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MoRTH,TAMIL NADU	03/2015	258.97 -	08/2015 -	-	0/0
507	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MoRTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-	0/0
508	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I- - [N24000318]MoRTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-	0/0
509	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MoRTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-	0/0
510	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA	01/2015	225.81 -	- -	-	0/0
511	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-	0/0
512	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MoRTH,KARNATAKA	03/2015	159.12 -	11/2015 -	-	0/0
513	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]MoRTH,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	-	0/0
514	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]MoRTH,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	-	0/0
515	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]MoRTH,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	-	0/0
516	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MoRTH,KARNATAKA	01/1991	219.40 -	01/2018 -	-	0/0
517	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MoRTH,ODISHA	01/1991	218.63 -	10/2017 -	-	0/0
518	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH,BIHAR	01/1991	675.00 -	- -	-	0/0
519	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]MoRTH,PUNJAB	12/2015	766.36 -	- 09/2019	-	0/0
520	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]MoRTH,PUNJAB	11/2015	847.02 -	- 12/2019	-	0/0
521	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]MoRTH,PUNJAB	11/2015	889.24 904.82	- 05/2020	-	0/0
522	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]MoRTH,ASSAM	11/2010	268.08 -	05/2017 -	-	0/0
523	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]MoRTH,MADHYA PRADESH	08/2015	257.80 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
524	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]MoRTH,ASSAM	11/2010	470.20 -	02/2011 -	-	0/0
525	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MoRTH, WEST BENGAL	01/1991	322.00 -	03/2018 -	-	0/0
526	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MoRTH, BIHAR	01/1991	282.41 -	08/2016 -	-	0/0
527	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MoRTH, BIHAR	01/1991	358.22 -	10/2016 -	-	0/0
528	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]MoRTH, ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-	0/0
529	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]MoRTH, ASSAM	11/2014	218.31 -	02/2018 -	-	0/0
530	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MoRTH, ODISHA	01/1991	229.41 -	05/2018 -	-	0/0
531	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]MoRTH, ODISHA	07/2014	342.05 -	01/2017 -	-	0/0
532	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH, GOA	10/2015	936.40 -	- -	-	0/0
533	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]MoRTH, RAJASTHAN	09/2012	511.00 -	10/2013 -	-	0/0
534	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH, GOA	12/2015	773.98 -	- -	-	0/0
535	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MoRTH, GOA	12/2015	819.95 -	- -	-	0/0
536	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MoRTH, BIHAR	01/1991	478.35 -	- -	-	0/0
537	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]MoRTH, ODISHA	12/2011	159.39 -	11/2017 -	-	0/0
538	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]MoRTH, PUNJAB	06/2015	892.17 -	- 02/2018	-	0/0
539	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH, ODISHA	12/2011	191.08 -	08/2015 -	-	0/0
540	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]MoRTH, BIHAR	01/1991	154.62 -	- -	-	0/0
541	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]MoRTH, BIHAR	01/1991	319.68 -	- -	-	0/0
542	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MoRTH, BIHAR	10/2013	278.39 -	08/2014 -	-	0/0
543	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MoRTH, BIHAR	11/2013	683.83 -	07/2016 -	-	0/0
544	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MoRTH, BIHAR	02/2014	665.50 -	07/2016 -	-	0/0
545	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MoRTH, BIHAR	02/2016	178.85 -	05/2016 -	-	0/0
546	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MoRTH, BIHAR	02/2016	369.77 -	06/2016 -	-	0/0
547	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MoRTH, BIHAR	02/2016	553.30 -	05/2016 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
548	FOUR LANEING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-	0/0
549	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPR - [N24000580]MoRTH,BIHAR	03/2015	206.80 -	07/2016 -	-	0/0
550	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MoRTH,BIHAR	08/2015	288.24 -	11/2015 -	-	0/0
551	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH,MAHARASHTRA	03/2016	1,142.62 -	- -	-	0/0
552	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH,MAHARASHTRA	03/2016	1,101.58 -	- -	-	0/0
553	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH,BIHAR	08/2016	1,742.01 -	12/2016 -	-	0/0
554	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH,ODISHA	03/2014	191.50 192.00	05/2016 -	-	0/0
555	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MoRTH,ODISHA	01/2015	326.63 327.00	04/2018 -	-	0/0
556	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MoRTH,ODISHA	02/2015	239.91 240.00	10/2017 -	-	0/0
557	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MoRTH,ODISHA	07/2014	342.05 342.00	01/2017 -	-	0/0
558	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH,ODISHA	08/2013	171.96 172.00	06/2016 -	-	0/0
559	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MoRTH,ODISHA	06/2016	157.30 157.00	06/2018 -	-	0/0
560	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH,UTTARAKHAND	12/2017	257.34 -	12/2019 -	-	0/0
561	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH,UTTARAKHAND	12/2017	200.34 -	12/2019 -	-	0/0
562	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MoRTH,UTTARAKHAND	12/2017	248.22 -	12/2019 -	-	0/0
563	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MoRTH,UTTARAKHAND	06/2017	282.08 -	06/2019 -	-	0/0
564	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2-LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH,UTTARAKHAND	11/2017	232.81 -	11/2019 -	-	0/0
565	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH,UTTARAKHAND	11/2017	283.51 -	11/2019 -	-	0/0
566	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH,UTTARAKHAND	11/2017	266.52 -	11/2019 -	-	0/0
567	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MoRTH,UTTARAKHAND	02/2018	293.68 -	- -	-	0/0
568	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH,UTTARAKHAND	03/2018	460.73 -	- -	-	0/0
569	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MoRTH,A & N ISLANDS	11/2017	237.80 -	11/2019 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
570	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH,A & N ISLANDS	11/2017	257.34 -	11/2019 -	-	0/0
571	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]MoRTH,WEST BENGAL	01/2017	396.86 396.86	09/2019 -	-	0/0
572	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH	11/2016	326.99 327.00	- -	-	0/0
573	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879]MoRTH,WEST BENGAL	03/2017	202.69 202.69	11/2019 -	-	0/0
574	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]MoRTH,WEST BENGAL	02/2018	426.18 426.18	09/2020 -	-	0/0
575	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]MoRTH,WEST BENGAL	02/2018	218.70 218.70	11/2020 -	-	0/0
576	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) - [N24000908]MoRTH,HARYANA	01/2017	276.01 -	03/2019 07/2019	-	0/0
577	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26. - [N24000911]MoRTH,ODISHA	03/2016	165.06 -	12/2016 -	-	0/0
578	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MoRTH,ODISHA	08/2016	287.70 -	02/2017 -	-	0/0
579	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH,ODISHA	09/2016	295.67 -	02/2017 -	-	0/0
580	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH,ODISHA	12/2016	223.50 -	08/2018 -	-	0/0
581	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH,ODISHA	12/2016	206.88 -	04/2018 -	-	0/0
582	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH,ODISHA	03/2018	214.23 -	08/2018 -	-	0/0
583	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH,ODISHA	03/2018	199.16 -	08/2018 -	-	0/0
584	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR	09/2018	1,478.40 -	- -	-	0/0
585	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH,TELANGANA	01/2017	244.54 -	05/2019 -	-	0/0
586	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]MoRTH,TELANGANA	01/2017	196.52 -	10/2019 -	-	0/0
587	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]MoRTH,TELANGANA	01/2017	283.00 -	12/2019 -	-	0/0
588	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]MoRTH,TELANGANA	01/2017	359.27 -	05/2019 -	-	0/0
589	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]MoRTH,TELANGANA	01/2018	230.03 -	12/2019 -	-	0/0
590	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH,TELANGANA	02/2018	294.13 -	11/2019 -	-	0/0
591	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH,TELANGANA	02/2018	220.28 -	11/2019 -	-	0/0
592	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH,TELANGANA	01/2017	605.08 -	10/2019 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
593	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH,TELANGANA	03/2018	192.67 -	07/2019 -	-	0/0
594	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH,TELANGANA	01/2019	193.19 -	- -	-	0/0
595	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C - [N24000999]MoRTH,BIHAR	11/2016	230.34 -	10/2019 -	-	0/0
596	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH,BIHAR	03/2018	153.24 -	- -	-	0/0
597	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA	01/2017	341.16 341.00	06/2019 -	-	0/0
598	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH,MAHARASHTRA	01/2017	471.61 472.00	06/2019 -	-	0/0
599	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA	01/2017	392.83 393.00	06/2019 -	-	0/0
600	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA	01/2017	232.77 -	07/2019 -	-	0/0
601	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA	02/2017	422.02 422.00	07/2019 -	-	0/0
602	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA	01/2017	388.44 -	- -	-	0/0
603	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA	02/2017	406.51 -	06/2019 -	-	0/0
604	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND	08/2016	234.88 -	12/2017 -	-	0/0
605	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	-	0/0
606	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT - [N24001154]MoRTH,KARNATAKA	08/2016	367.44 -	01/2017 -	-	0/0
607	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT - [N24001155]MoRTH,KARNATAKA	08/2016	175.20 -	01/2017 -	-	0/0
608	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA - [N24001156]MoRTH,KARNATAKA	01/2017	166.67 -	09/2017 -	-	0/0
609	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA	08/2016	175.50 -	02/2017 -	-	0/0
610	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA	03/2018	159.97 -	06/2019 -	-	0/0
611	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]MoRTH,KARNATAKA	01/2018	159.70 -	07/2018 -	-	0/0
612	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA	09/2017	191.60 -	10/2018 -	-	0/0
613	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]MoRTH,KARNATAKA	12/2017	297.30 -	01/2019 -	-	0/0
614	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA	03/2018	325.86 -	10/2018 -	-	0/0
615	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]MoRTH,KARNATAKA	08/2016	329.01 -	02/2017 -	-	0/0
616	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA	10/2016	396.96 -	03/2017 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
617	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA	11/2016	314.90 -	03/2017 -	-	0/0
618	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA	03/2015	159.12 -	01/2016 -	-	0/0
619	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776) - [N24001167]MoRTH,KARNATAKA	03/2015	165.67 -	01/2016 -	-	0/0
620	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM. - [N24001170]MoRTH,KARNATAKA	01/2014	471.16 -	08/2014 -	-	0/0
621	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA	01/2017	291.49 -	08/2017 -	-	0/0
622	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND	11/2016	336.25 -	09/2019 -	-	0/0
623	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S - [N24001183]MoRTH,ANDHRA PRADESH	07/2014	251.55 -	02/2015 -	-	0/0
624	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH,ARUNACHAL PRADESH	09/2011	1,979.00 -	- 03/2020	-	0/0
625	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MoRTH,RAJASTHAN	03/2019	178.13 -	- -	-	0/0
626	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR	02/2019	2,926.42 -	- -	-	0/0
627	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH,UTTAR PRADESH	03/2018	306.59 -	- -	-	0/0
628	IMPROVEMENT AND UP-GRADATION OF EXISITING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH,UTTAR PRADESH	11/2018	281.45 -	- -	-	0/0
629	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]MoRTH,CHHATISGARH	01/2016	497.14 -	08/2016 -	-	0/0
630	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218]MoRTH,CHHATISGARH	11/2015	335.32 -	06/2017 -	-	0/0
631	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]MoRTH,CHHATISGARH	01/2016	476.20 544.00	09/2016 -	-	0/0
632	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 127.500 TO 178.944 DARRIGHAT TO BANARI SECTION - [N24001220]MoRTH,CHHATISGARH	03/2016	491.52 -	09/2016 -	-	0/0
633	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]MoRTH,CHHATISGARH	01/2016	624.98 -	10/2016 -	-	0/0
634	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222]MoRTH,CHHATISGARH	03/2016	452.94 -	07/2016 -	-	0/0
635	WIDENING OF SL TO 2 L KM. 107-184.80 SUKUMA TO KONTA ON NH 221 - [N24001223]MoRTH,CHANDIGARH	03/2010	179.89 271.00	03/2013 -	-	0/0
636	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO - [N24001224]MoRTH,CHHATISGARH	03/2017	423.79 -	01/2018 -	-	0/0
637	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1 - [N24001225]MoRTH,CHANDIGARH	12/2010	169.26 299.00	01/2019 -	-	0/0
638	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226]MoRTH,CHHATISGARH	12/2014	496.02 -	03/2015 -	-	0/0
639	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228]MoRTH,CHHATISGARH	11/2017	188.80 -	05/2019 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
640	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 - [N24001229]MoRTH, CHHATISGARH	12/2014	379.16 -	11/2017 -	-	0/0
641	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]MoRTH, MIZORAM	08/2010	195.04 -	10/2010 12/2020	06/2020	0/0
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>					
642	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL, ARUNACHAL PRADESH	10/2015	210.50 210.50	- 01/2016	01/2019	0/0
643	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL, MIZORAM	04/2017	519.09 -	09/2019 -	09/2019	0/0
644	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL, MIZORAM	04/2017	640.07 -	09/2019 -	09/2019	0/0
645	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL, MIZORAM	04/2017	642.96 -	09/2019 -	09/2019	0/0
646	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL, MIZORAM	04/2017	473.18 -	09/2019 -	09/2019	0/0
647	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL, MIZORAM	04/2017	537.82 -	09/2019 -	09/2019	0/0
648	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL, MIZORAM	04/2017	518.53 -	09/2019 -	09/2019	0/0
649	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL, MIZORAM	04/2017	404.29 -	09/2019 -	09/2019	0/0
650	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL, MIZORAM	04/2017	428.11 -	09/2019 -	09/2019	0/0
651	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D - [N24000974]NHIDCL, ARUNACHAL PRADESH	02/2017	199.02 199.02	- 02/2018	02/2021	0/0
652	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D - [N24000975]NHIDCL, ARUNACHAL PRADESH	02/2017	184.88 184.88	- 02/2018	02/2021	0/0
653	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL, ARUNACHAL PRADESH	02/2017	175.06 175.06	- 04/2019	04/2022	0/0
654	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL, ARUNACHAL PRADESH	02/2017	176.12 176.12	- 04/2019	04/2022	0/0
655	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL, NAGALAND	03/2018	500.09 336.49	09/2018 -	-	0/0
656	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL, NAGALAND	03/2018	339.57 233.35	09/2018 07/2019	-	0/0
657	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL, SIKKIM	03/2017	375.80 -	- -	-	0/0
658	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITTA AND PANITNAKI I - [N24000770]NHIDCL, WEST BENGAL	03/2017	158.65 -	06/2018 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
659	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR	03/2018	253.44 -	07/2019 -	-	0/0
660	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH	12/2016	200.44 -	- -	-	0/0
661	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH	03/2017	1,718.59 -	- -	-	0/0
662	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 37.500 TO KM - [N24000947]NHIDCL,ARUNACHAL PRADESH	05/2016	259.52 -	- -	-	0/0
663	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH	09/2016	568.92 -	- -	-	0/0
664	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH	12/2016	188.78 -	- -	-	0/0
665	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8 - [N24001184]NHIDCL,DELHI	07/2017	269.69 -	09/2019 -	-	0/0
666	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL,ASSAM	03/2017	1,049.51 -	- -	-	0/0
National Highways Authority Of India						
667	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL	10/2015	361.15 -	- -	01/2020	0/0
668	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	08/2018 -	01/2020	0/0
669	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	04/2019	0/0
670	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 255.23	11/2008 01/2011	08/2013	0/0
671	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 435.78	11/2008 07/2011	01/2014	0/0
672	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- 06/2015	06/2015	0/0
673	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- 06/2015	06/2015	0/0
674	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	10/2017	0/0
675	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 03/2018	03/2018	0/0
676	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	04/2018 08/2018	08/2018	0/0
677	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 655.17	07/2009 10/2018	10/2018	0/0
678	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA	09/2016	1,004.67 -	05/2019 -	02/2019	0/0
679	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 -	03/2019	0/0
680	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 -	06/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
681	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 725.87	02/2019 -	06/2019	0/0
682	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 520.00	02/2009 07/2019	07/2019	0/0
683	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	04/2010 -	07/2019	0/0
684	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	11/2017 -	07/2019	0/0
685	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 340.14	04/2009 03/2011	08/2019	0/0
686	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 -	09/2019	0/0
687	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 -	06/2019 12/2016	09/2019	0/0
688	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	06/2019 -	09/2019	0/0
689	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	06/2019 -	09/2019	0/0
690	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 767.03	08/2018 -	09/2019	0/0
691	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	09/2019	0/0
692	TWO LANING WITH PAVED SHOULDER OF KARAU - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 09/2014	10/2019	0/0
693	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	05/2018 10/2019	10/2019	0/0
694	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	05/2018 03/2018	10/2019	0/0
695	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	- 02/2016	10/2019	0/0
696	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 537.16	07/2018 -	11/2019	0/0
697	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	04/2019 -	11/2019	0/0
698	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	11/2019	0/0
699	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	12/2019	0/0
700	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 507.70	06/2016 -	12/2019	0/0
701	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 637.86	- -	12/2019	0/0
702	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	- -	12/2019	0/0
703	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS- WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	- 12/2017	12/2019	0/0
704	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	05/2019 -	12/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
705	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- -	01/2020	0/0
706	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	01/2020	0/0
707	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	01/2020	0/0
708	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB	03/2018	196.05 149.90	- -	01/2020	0/0
709	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	- -	02/2020	0/0
710	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 881.00	- 05/2017	02/2020	0/0
711	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	- -	02/2020	0/0
712	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	07/2018 12/2019	02/2020	0/0
713	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA	03/2017	247.02 -	03/2020 02/2021	02/2020	0/0
714	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	04/2008 -	03/2020	0/0
715	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 364.59	12/2009 08/2020	03/2020	0/0
716	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	03/2020	0/0
717	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 2,967.50	11/2011 -	03/2020	0/0
718	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	03/2020	0/0
719	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 12/2019	03/2020	0/0
720	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 585.00	11/2013 12/2019	03/2020	0/0
721	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	03/2020	0/0
722	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	07/2017 12/2019	03/2020	0/0
723	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 659.57	- -	03/2020	0/0
724	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 -	03/2018 -	03/2020	0/0
725	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	08/2018 -	03/2020	0/0
726	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 67.34	01/2018 12/2018	03/2020	0/0
727	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 598.13	04/2018 03/2020	03/2020	0/0
728	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	- -	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
729	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	08/2018 -	03/2020	0/0
730	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	06/2018 -	03/2020	0/0
731	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 2,541.32	09/2019 03/2020	03/2020	0/0
732	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	05/2019 -	03/2020	0/0
733	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 315.00	- 03/2020	03/2020	0/0
734	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 -	03/2020 -	03/2020	0/0
735	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA	03/2017	744.64 -	03/2020 -	03/2020	0/0
736	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA	03/2017	296.19 -	03/2020 -	03/2020	0/0
737	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA	03/2017	639.79 -	03/2020 -	03/2020	0/0
738	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR	03/2017	672.89 -	03/2020 -	03/2020	0/0
739	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]NHAI,ANDHRA PRADESH	03/2017	648.32 -	03/2020 -	03/2020	0/0
740	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]NHAI,JHARKHAND	03/2017	165.50 -	03/2020 -	03/2020	0/0
741	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI,JHARKHAND	03/2017	239.68 -	03/2020 -	03/2020	0/0
742	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	- -	03/2020	0/0
743	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA	03/2018	275.12 -	- -	03/2020	0/0
744	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTI - [N24000837]NHAI,HARYANA	03/2018	307.79 -	- -	03/2020	0/0
745	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA	03/2018	198.05 -	- -	03/2020	0/0
746	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA	03/2018	551.58 -	- -	03/2020	0/0
747	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 2,257.49	07/2018 -	04/2020	0/0
748	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 3,007.86	06/2018 -	04/2020	0/0
749	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	- -	04/2020	0/0
750	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 1,367.00	- -	04/2020	0/0
751	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20 -	04/2020 -	04/2020	0/0
752	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN	04/2017	894.00 -	04/2020 -	04/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
753	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	04/2020	0/0
754	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	05/2020	0/0
755	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	07/2018 -	05/2020	0/0
756	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	- -	05/2020	0/0
757	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 911.07	02/2020 11/2017	05/2020	0/0
758	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 2,602.09	03/2020 11/2017	05/2020	0/0
759	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	05/2020	0/0
760	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	07/2016 -	05/2020	0/0
761	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 3,207.63	- 02/2018	05/2020	0/0
762	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	06/2020	0/0
763	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014 04/2017	06/2020	0/0
764	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	06/2020	0/0
765	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	- -	06/2020	0/0
766	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 897.03	11/2018 07/2019	06/2020	0/0
767	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 2,182.03	06/2018 -	06/2020	0/0
768	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 2,433.38	06/2018 -	06/2020	0/0
769	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 746.43	12/2017 06/2020	06/2020	0/0
770	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH	03/2017	2,064.99 -	03/2020 06/2020	06/2020	0/0
771	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	03/2020 -	06/2020	0/0
772	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	- 06/2020	06/2020	0/0
773	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA	03/2018	181.78 -	- -	06/2020	0/0
774	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	07/2020	0/0
775	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	04/2019 07/2020	07/2020	0/0
776	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	- -	07/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
777	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	07/2020	0/0
778	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	03/2020 -	07/2020	0/0
779	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 -	08/2020	0/0
780	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 01/2019	08/2020	0/0
781	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	10/2013 -	08/2020	0/0
782	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI,WEST BENGAL	03/2016	229.37 -	11/2018 08/2020	08/2020	0/0
783	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	- -	08/2020	0/0
784	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 870.00	03/2019 03/2017	08/2020	0/0
785	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	- -	08/2020	0/0
786	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	- -	08/2020	0/0
787	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH	06/2017	648.33 -	06/2017 -	08/2020	0/0
788	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	09/2017 -	08/2020	0/0
789	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 12/2019	09/2020	0/0
790	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	05/2018 -	09/2020	0/0
791	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	09/2020	0/0
792	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	08/2017 -	09/2020	0/0
793	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN	02/2018	1,103.88 -	- -	09/2020	0/0
794	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 09/2017	10/2020	0/0
795	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	- 10/2020	10/2020	0/0
796	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 448.18	- -	10/2020	0/0
797	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 11/2020	11/2020	0/0
798	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 11/2019	11/2020	0/0
799	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	03/2019 -	11/2020	0/0
800	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	03/2019 -	11/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
801	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 05/2018	11/2020	0/0
802	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	10/2017 -	11/2020	0/0
803	FOUR LANING OF CHETTICKULAM TO NATHAM SECTION OF NH-785 FROM CHETTICKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35 -	- -	11/2020	0/0
804	FOUR LANING OF MADURAI- CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICKULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	- -	11/2020	0/0
805	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53 -	- 11/2020	11/2020	0/0
806	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21 -	- -	11/2020	0/0
807	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	08/2016 -	12/2020	0/0
808	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	12/2020	0/0
809	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	04/2018 -	12/2020	0/0
810	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	07/2019 12/2020	12/2020	0/0
811	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	07/2019 12/2020	12/2020	0/0
812	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 1,008.00	08/2019 -	12/2020	0/0
813	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJI WAL (KM 283.500 OF NH 65 NAGPUR ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	- -	12/2020	0/0
814	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- 03/2020	12/2020	0/0
815	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43 -	- -	12/2020	0/0
816	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA	03/2018	1,484.30 -	- -	12/2020	0/0
817	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA	03/2018	642.13 -	- -	12/2020	0/0
818	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	- -	01/2021	0/0
819	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB	02/2018	261.76 -	- -	01/2021	0/0
820	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT	02/2018	1,052.21 1,449.00	- -	01/2021	0/0
821	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT	03/2018	2,702.05 -	- 05/2018	01/2021	0/0
822	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	03/2019 -	02/2021	0/0
823	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26 -	- -	02/2021	0/0
824	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH	03/2018	565.09 -	- -	02/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
825	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	03/2021	0/0
826	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	08/2019 -	03/2021	0/0
827	4-LANNING OF KODEBAD-DHANTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	03/2019 -	03/2021	0/0
828	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	- -	03/2021	0/0
829	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	03/2020 -	03/2021	0/0
830	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH	03/2018	1,029.96 -	- 03/2021	03/2021	0/0
831	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 1,073.10	- 03/2019	03/2021	0/0
832	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	03/2019 04/2021	04/2021	0/0
833	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU	03/2018	1,016.92 -	- -	04/2021	0/0
834	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA	03/2018	806.11 -	- -	04/2021	0/0
835	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	03/2020 -	05/2021	0/0
836	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	09/2017 -	05/2021	0/0
837	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH	03/2018	478.74 -	- -	05/2021	0/0
838	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	07/2017 11/2020	06/2021	0/0
839	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	- 07/2020	06/2021	0/0
840	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	- -	06/2021	0/0
841	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	- 05/2020	06/2021	0/0
842	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	- 05/2020	06/2021	0/0
843	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	- 03/2020	06/2021	0/0
844	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	- 06/2021	06/2021	0/0
845	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	- -	06/2021	0/0
846	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	- -	06/2021	0/0
847	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	- -	07/2021	0/0
848	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI,WEST BENGAL	03/2018	1,261.98 -	- -	07/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
849	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 -	- -	07/2021	0/0
850	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 1,730.07	- -	07/2021	0/0
851	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64 1,687.00	- 12/2018	07/2021	0/0
852	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA	03/2018	634.70 931.21	- -	07/2021	0/0
853	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA	03/2018	795.50 -	- -	07/2021	0/0
854	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 -	- -	07/2021	0/0
855	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	03/2020 -	08/2021	0/0
856	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	- -	08/2021	0/0
857	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPASS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	- -	08/2021	0/0
858	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	06/2020 -	09/2021	0/0
859	SIX-LANING OF BANGALORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 2,190.00	- 05/2019	11/2021	0/0
860	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	- -	12/2021	0/0
861	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	08/2017 -	02/2022	0/0
862	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-	0/0
863	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-	0/0
864	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-	0/0
865	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-	0/0
866	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	-	0/0
867	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	-	0/0
868	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-	0/0
869	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	-	0/0
870	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-	0/0
871	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	-	0/0
872	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
873	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	-	0/0
874	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	-	0/0
875	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	06/2015 -	-	0/0
876	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-	0/0
877	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	-	0/0
878	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	09/2016 -	-	0/0
879	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA	08/2015	723.54 1,286.84	02/2018 10/2017	-	0/0
880	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	-	0/0
881	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	01/2016 -	-	0/0
882	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH	06/2014	301.04 -	01/2016 -	-	0/0
883	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	01/2016 -	-	0/0
884	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	05/2019 -	-	0/0
885	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	05/2019 -	-	0/0
886	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	04/2018 -	-	0/0
887	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	04/2019 -	-	0/0
888	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	01/2019 -	-	0/0
889	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-	0/0
890	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 -	06/2018 -	-	0/0
891	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-	0/0
892	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	-	0/0
893	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	04/2019 -	-	0/0
894	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA	11/2015	867.66 1,464.24	05/2018 02/2018	-	0/0
895	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	-	0/0
896	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
897	FOUR LANNING FROM MP/MAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	-	0/0
898	SIX-LANNING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL	04/2014	1,665.00 -	- -	-	0/0
899	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-	0/0
900	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR-HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 151.11	07/2018 -	-	0/0
901	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	04/2019 -	-	0/0
902	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	11/2018 -	-	0/0
903	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 3,267.94	- 03/2017	-	0/0
904	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 -	03/2019 -	-	0/0
905	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-	0/0
906	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	04/2019 -	-	0/0
907	SIX-LANNING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 241.41	- -	-	0/0
908	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	10/2018 -	-	0/0
909	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-	0/0
910	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-	0/0
911	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	- -	-	0/0
912	6-LANNING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	- -	-	0/0
913	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-	0/0
914	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-	0/0
915	REHABILITATION AND UPGRADATION OF TWO LANNING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 -	- -	-	0/0
916	SIX LANNING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-	0/0
917	FOUR LANNING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-	0/0
918	SIX LANNING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-	0/0
919	FOUR LANNING OF DELINKED STRETCH OF SEONI - MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH	01/2018	960.24 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
920	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	-	0/0
921	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA	01/2018	633.68 -	- -	-	0/0
922	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 929.89	- -	-	0/0
923	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA	03/2017	4,429.00 -	03/2017 -	-	0/0
924	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA	02/2018	486.78 -	- -	-	0/0
925	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 -	- -	-	0/0
926	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 -	- -	-	0/0
927	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 2,283.50	- 10/2019	-	0/0
928	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 1,065.70	- -	-	0/0
929	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH	03/2018	925.40 1,197.00	- -	-	0/0
930	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN	02/2018	741.86 -	- -	-	0/0
931	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN	02/2018	716.76 -	- -	-	0/0
932	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	-	0/0
933	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 1,332.00	- -	-	0/0
934	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH	03/2018	1,025.80 -	- -	-	0/0
935	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH	03/2018	1,115.28 -	- -	-	0/0
936	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K - [N24000804]NHAI,TELANGANA	03/2018	802.65 -	- -	-	0/0
937	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-	0/0
938	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	- -	-	0/0
939	FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA	03/2018	950.63 -	- -	-	0/0
940	FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA	03/2018	857.62 -	- -	-	0/0
941	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI,TELANGANA	03/2018	828.29 998.89	- 11/2019	-	0/0
942	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU	03/2018	633.55 -	- -	-	0/0
943	FOUR LANING OF POONDYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU	03/2018	2,065.96 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
944	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE	03/2018	1,294.47 -	- -	-	0/0
945	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE	03/2018	998.70 -	- -	-	0/0
946	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT	03/2018	1,161.39 1,404.00	- 11/2021	-	0/0
947	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN	03/2018	874.25 -	- -	-	0/0
948	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN	03/2018	1,158.35 -	- -	-	0/0
949	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB	03/2018	199.90 149.90	- -	-	0/0
950	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - [N24001185]NHAI,UTTAR PRADESH	11/2017	2,159.00 -	01/2019 -	-	0/0
951	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI,HARYANA	01/2019	1,051.91 -	- -	-	0/0
952	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI,HARYANA	01/2019	1,120.06 -	- -	-	0/0
953	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA	01/2019	1,137.42 -	- -	-	0/0
954	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA	01/2019	1,033.19 -	- -	-	0/0
955	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA	01/2019	1,243.45 -	- -	-	0/0
956	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA	01/2019	889.36 -	- -	-	0/0
957	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA	01/2019	1,018.79 -	- -	-	0/0
958	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA	01/2019	996.65 -	- -	-	0/0
959	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI,MADHYA PRADESH	10/2019	743.88 -	- -	-	0/0
960	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]NHAI,MADHYA PRADESH	12/2017	656.98 -	- -	-	0/0
961	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA - [N24001213]NHAI,MADHYA PRADESH	12/2017	1,094.97 -	- -	-	0/0
962	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214]NHAI,MADHYA PRADESH	12/2017	217.96 -	- -	-	0/0
963	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 275.00	05/2017 -	-	0/0
964	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	12/2017 -	-	0/0
965	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 1,444.25	- 02/2019	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	<u>SHIPPING AND PORTS</u>					
	<u>Inland Waterways Authority Of India</u>					
966	JAL MARG VIKAS PROJECT - [N25000072]IWAI, MULTI STATE	01/2018	4,200.00 5,369.18	03/2023 03/2023	03/2023	0/0
	<u>TELECOMMUNICATIONS</u>					
	<u>Bharat Sanchar Nigam Limited</u>					
967	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]BSNL, MAHARASHTRA	01/2018	231.80 240.10	10/2018 02/2020	02/2020	0/0
	<u>Department Of Telecommunication</u>					
968	NETWORK FOR SPECTRUM - [N26000101]DOT, MULTI STATE	03/2012	13,334.00 -	07/2015 -	05/2020	0/0
	<u>Mahanagar Telephone Nigam Limited</u>					
969	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL, DELHI	06/2016	418.26 -	06/2017 -	-	0/0
	<u>URBAN DEVELOPMENT</u>					
	<u>Ahmedabad Metro Rail</u>					
970	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA, GUJARAT	11/2014	10,773.00 -	12/2018 -	07/2020	0/0
971	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137]MEGA, GUJARAT	03/2019	5,384.17 -	03/2024 -	03/2024	0/0
972	SURAT METRO RAIL PROJECT - [N28000138]MEGA, GUJARAT	03/2019	12,020.32 -	03/2024 -	03/2024	0/0
	<u>Bangalore Metro Rail Corporation Limited</u>					
973	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL, KARNATAKA	02/2014	26,405.14 -	02/2019 -	03/2020	0/0
	<u>Central Public Works Department</u>					
974	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD, UTTAR PRADESH	11/2017	171.72 -	03/2020 11/2020	03/2020	0/0
975	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD, DELHI	10/2016	248.20 -	04/2018 02/2020	08/2020	0/0
976	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD, DELHI	10/2017	271.90 -	11/2019 08/2020	08/2020	0/0
977	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD, DELHI	10/2016	422.00 -	- 03/2021	12/2020	0/0
978	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD, DELHI	10/2016	392.00 -	- 08/2020	03/2021	0/0
979	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD, HIMACHAL PRADESH	12/2018	260.00 -	06/2021 -	06/2021	0/0
980	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I - [N28000128]CPWD, DELHI	10/2016	1,180.00 -	07/2021 -	07/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
981	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]CPWD,DELHI	10/2016	1,128.00 -	03/2022 -	03/2022	0/0
982	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	12/2015 -	-	0/0
983	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	12/2013 -	-	0/0
984	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130]CPWD,JAMMU AND KASHMIR	03/2019	329.00 -	- -	-	0/0
985	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]CPWD,JAMMU AND KASHMIR	01/2018	676.00 -	- -	-	0/0
	<u>Delhi Metro Rail Corporation</u>					
986	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136]DMRC,DELHI	05/2017	565.00 -	12/2020 -	12/2020	0/0
987	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS - [N28000135]DMRC,DELHI	07/2019	24,948.65 -	03/2025 -	03/2025	0/0
988	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	03/2016 -	-	0/0
	<u>Hindustan Steelwork Construction Limited</u>					
989	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	03/2015 -	03/2021	0/0
990	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	12/2015 -	-	0/0
991	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	12/2016 -	-	0/0
992	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	12/2016 -	-	0/0
993	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,070.97	02/2014 -	-	0/0
994	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 324.87	12/2015 -	-	0/0
995	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	09/2017 -	-	0/0
996	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	- -	-	0/0
997	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL,GUJARAT	01/2013	175.00 -	- -	-	0/0
998	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	03/2017 -	-	0/0
999	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 253.92	06/2016 -	-	0/0
1000	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND	12/2007	200.00 -	03/2018 -	-	0/0
1001	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	12/2016 -	-	0/0
1002	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND	04/2013	170.00 -	04/2018 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
1003	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL, WEST BENGAL	08/2012	185.37 -	03/2016 -	-	0/0
	<u>Jawahar Lal Nehru National Urban Renewal Mission</u>					
1004	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM, ANDHRA PRADESH	08/2007	246.90 -	- -	-	0/0
	<u>Kochi Metro Rail Corporation Ltd</u>					
1005	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL, KERALA	07/2012	5,181.79 5,687.79	07/2017 -	03/2020	0/0
	<u>Lucknow Metro Rail Corporation Limited</u>					
1006	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL, UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	-	0/0
	<u>Maharashtra Metro Rail Corporation Ltd.</u>					
1007	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC, MAHARASHTRA	12/2016	11,420.00 11,420.00	11/2021 03/2022	03/2022	0/0
	<u>Mumbai Metro Rail Corporation Ltd</u>					
1008	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL, MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	05/2020	0/0
	<u>Madhya Pradesh Metro Rail Co Limited</u>					
1009	BHOPAL METRO RAIL - [N28000124]MPMRCL, MADHYA PRADESH	11/2018	6,941.40 -	02/2023 -	02/2023	0/0
1010	INDORE METRO RAIL - [N28000125]MPMRCL, MADHYA PRADESH	11/2018	7,500.80 -	02/2023 -	02/2023	0/0
	<u>Nagpur Metro Rail Corporation Ltd</u>					
1011	NAGPUR METRO RAIL - [N28000085]NMRCL, MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	12/2019	0/0
	<u>National Building Construction Corporation Ltd</u>					
1012	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC, DELHI	07/2016	2,694.00 -	- -	-	0/0
	<u>National Capital Region Transport Corp</u>					
1013	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134]NCRTC, MULTI STATE	03/2019	30,274.00 -	06/2025 -	06/2025	0/0
	<u>WATER RESOURCES</u>					
	<u>Brahmaputra Board</u>					
1014	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPPB, MAHARASHTRA	03/2017	233.57 -	12/2019 -	-	0/0
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>					
1015	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]BUIDCO, BIHAR	12/2014	225.77 -	03/2020 -	03/2020	0/0
1016	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR - [N30000038]BUIDCO, BIHAR	04/2015	184.93 -	04/2020 -	04/2020	0/0
1017	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO, BIHAR	10/2017	254.13 -	09/2020 -	09/2020	0/0
1018	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]BUIDCO, BIHAR	05/2017	191.62 -	11/2020 -	11/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
1019	I AND D AND STP AT CHAPPRA - [N30000028]BUIDCO,BIHAR	11/2018	236.15 -	12/2020 -	12/2020	0/0
1020	SAIDPUR SEWER NETWORK PATNA - [N30000039]BUIDCO,BIHAR	04/2015	268.63 -	01/2021 -	01/2021	0/0
1021	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]BUIDCO,BIHAR	05/2017	356.37 -	04/2021 -	04/2021	0/0
1022	SEWERAGE SCHEME AT PAHARI ZONE IVA S PATNA - [N30000041]BUIDCO,BIHAR	05/2017	184.86 -	05/2021 -	05/2021	0/0
1023	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]BUIDCO,BIHAR	03/2017	277.42 -	05/2021 -	05/2021	0/0
1024	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026]BUIDCO,BIHAR	03/2018	230.06 -	07/2021 -	07/2021	0/0
1025	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]BUIDCO,BIHAR	03/2018	305.19 -	08/2021 -	08/2021	0/0
1026	SEWER NETWORKS, SPS AND STP, MUNGER - [N30000036]BUIDCO,BIHAR	03/2018	294.02 -	10/2021 -	10/2021	0/0
1027	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]BUIDCO,BIHAR	08/2017	578.89 -	06/2022 -	06/2022	0/0
1028	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA - [N30000051]BUIDCO,BIHAR	08/2017	824.00 -	06/2022 -	06/2022	0/0
	<u>Delhi Jal Board</u>					
1029	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018]DJB,DELHI	05/2017	344.81 -	05/2020 -	05/2020	0/0
1030	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI - [N30000017]DJB,DELHI	12/2018	515.07 -	01/2021 -	01/2021	0/0
1031	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015]DJB,DELHI	05/2016	211.79 -	12/2021 -	12/2021	0/0
1032	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]DJB,DELHI	05/2016	239.11 -	02/2022 -	02/2022	0/0
1033	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014]DJB,DELHI	03/2017	665.78 -	12/2022 -	12/2022	0/0
	<u>Kolkata Metropolitan Development Authority</u>					
1034	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046]KMDA,WEST BENGAL	02/2014	274.76 -	12/2019 02/2020	02/2020	0/0
1035	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]KMDA,WEST BENGAL	12/2014	272.32 -	04/2020 -	04/2020	0/0
1036	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]KMDA,WEST BENGAL	08/2017	185.22 -	12/2021 -	12/2021	0/0
1037	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048]KMDA,WEST BENGAL	01/2018	172.10 -	12/2021 -	12/2021	0/0
1038	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]KMDA,WEST BENGAL	10/2017	164.93 -	12/2021 -	12/2021	0/0
1039	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]KMDA,WEST BENGAL	05/2018	198.43 -	02/2022 -	02/2022	0/0
1040	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH - [N30000042]KMDA,WEST BENGAL	05/2018	160.00 -	02/2022 -	02/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
1041	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]KMDA, WEST BENGAL	01/2019	384.96 -	04/2022 -	04/2022	0/0
1042	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPUR - [N30000030]KMDA, WEST BENGAL	03/2019	287.53 -	04/2022 -	04/2022	0/0
1043	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]KMDA, WEST BENGAL	12/2018	234.31 -	04/2022 -	04/2022	0/0
1044	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033]KMDA, WEST BENGAL	03/2018	165.16 -	06/2022 -	06/2022	0/0
1045	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA - [N30000034]KMDA, WEST BENGAL	08/2017	307.12 -	09/2022 -	09/2022	0/0
<u>Uttar Pradesh Jal Nigam</u>						
1046	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA - [N30000011]UPJalNigam, UTTAR PRADESH	02/2017	161.31 -	11/2019 02/2020	02/2020	0/0
1047	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020]UPJalNigam, UTTAR PRADESH	02/2011	279.91 -	12/2019 03/2020	03/2020	0/0
1048	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR - [N30000009]UPJalNigam, UTTAR PRADESH	10/2016	370.40 430.49	08/2020 -	08/2020	0/0
1049	MATHURA SEWERAGE SCHEME - [N30000019]UPJalNigam, UTTAR PRADESH	12/2017	460.45 -	12/2020 -	12/2020	0/0
1050	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]UPJalNigam, UTTAR PRADESH	03/2019	298.12 -	07/2021 -	07/2021	0/0
1051	REHABILITATION RENOVATION OF AGRA SEWERAGE SCHEME INTERCEPTION AND DIVERSION WORKS IN AGRA UTTAR PR - [N30000012]UPJalNigam, UTTAR PRADESH	12/2018	857.26 -	08/2021 -	08/2021	0/0
1052	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH - [N30000013]UPJalNigam, UTTAR PRADESH	03/2019	271.39 -	08/2021 -	08/2021	0/0
1053	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WORKS AT AGRA - [N30000023]UPJalNigam, UTTAR PRADESH	02/2019	317.19 -	08/2021 -	08/2021	0/0
1054	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006]UPJalNigam, UTTAR PRADESH	05/2017	767.59 -	09/2021 -	09/2021	0/0
1055	INTEGRATED PROJECT FOR DEVELOPMENT OF STPS IN ALLAHABAD ALONG WITH EXISTING ASSETS - [N30000007]UPJalNigam, UTTAR PRADESH	03/2018	904.00 -	09/2021 -	09/2021	0/0
1056	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010]UPJalNigam, UTTAR PRADESH	03/2018	967.23 -	09/2021 -	09/2021	0/0
1057	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022]UPJalNigam, UTTAR PRADESH	01/2019	206.05 -	10/2021 -	10/2021	0/0
1058	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]UPJalNigam, UTTAR PRADESH	01/2019	231.79 -	12/2021 -	12/2021	0/0
1059	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]UPJalNigam, UTTAR PRADESH	10/2017	213.62 -	03/2022 -	03/2022	0/0
1060	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]UPJalNigam, UTTAR PRADESH	02/2019	681.78 -	06/2022 -	06/2022	0/0
<u>Uttarakhand Pey Jal Nigam</u>						
1061	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI - [N30000003]UKJalNigam, UTTARAKHAND	03/2017	273.37 -	08/2019 02/2020	02/2020	0/0
1062	INTERCEPTION AND DIVERSION (I&D) WITH STP AT RISHIKESH - [N30000004]UKJalNigam, UTTARAKHAND	03/2017	158.00 -	11/2019 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (January 2020)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>COMMERCE AND INDUSTRY</u>					
	<u>Delhi Mumbai Industrial Corridor</u>					
1063	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]DMIC,MULTI STATE	09/2011	12,579.09 -	09/2019 -	09/2020	0/0
	<u>India International Convention And Expo Centre</u>					
1064	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]IICC,DELHI	11/2017	4,773.00 -	12/2019 -	09/2020	0/0
	<u>HUMAN RESOURCE DEVELOPMENT</u>					
	<u>Central Public Works Department</u>					
1065	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA. - [N42000002]CPWD,GOA	05/2019	303.90 -	03/2020 -	03/2020	0/0
	<u>Edcil(India) Limited</u>					
1066	STUDY IN INDIA - [N42000003]EDCIL,MULTI STATE	03/2018	150.00 -	04/2018 -	-	0/0
	<u>Indian Institute Of Technology, Kharagpur</u>					
1067	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION - [N42000004]IITKGP,MULTI STATE	08/2018	418.00 -	03/2019 -	-	0/0
	<u>Rail India Technical And Economic Service</u>					
1068	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]RITES,MEGHALAYA	09/2013	484.32 -	09/2014 -	12/2020	0/0
	Total		12,52,584.68 -			0/0
	Grand Total		12,52,584.68			0/0

List of Projects Ahead of Schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>FERTILISERS</u>						
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
1	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018	4/2018	426.72 -	426.72	268.46	04/2020 07/2020	04/2020
	Total		426.72 -	426.72	268.46		
	<u>PETROLEUM</u>						
	<u>Indian Oil Corporation Limited</u>						
2	PARADIP HYDERABAD PIPELINE - [N16000194	1/2015	2,321.00 3,338.00	3,338.00	2,123.21	12/2020 -	08/2020
3	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252	5/2016	664.00 -	729.40	664.73	12/2020 -	02/2020
4	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302	8/2017	384.58	384.58	134.67	04/2021 -	09/2020
5	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254	9/2015	324.00 -	324.00	199.72	06/2020 -	03/2020
6	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332	3/2018	3,712.00 -	3,696.00	1,001.53	09/2022 -	06/2021
7	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308	8/2017	315.00 -	315.00	124.98	12/2021 -	12/2020
	Total		7,720.58 -	8,786.98	4,248.84		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
8	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192	1/2013	12,964.60 17,304.00	17,304.00	14,367.00	05/2018 12/2021	06/2021
	<u>Power Grid Corporation Of India Limited</u>						
9	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164	5/2014	522.29 546.36	546.36	470.71	11/2016 06/2020	03/2020
10	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242	2/2017	322.30 -	322.30	166.84	02/2019 04/2020	03/2020
	Total		13,809.19 -	18,172.66	15,004.55		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						

Costing Rs. 150 Crore and above

(January 2020)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
11	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	2/2015	3,627.47 -	3,627.47	854.93	03/2024 -	03/2023
	<u>East Central Railways</u>						
12	GARHWA ROAD-RAMNA - [N22000465]	3/2015	348.23 -	348.23	211.06	03/2021 -	12/2020
	<u>North East Frontier Railway</u>						
13	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	4/2015	2,232.32 -	2,182.00	765.94	03/2022 -	03/2020
14	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) [N22000390]	4/2016	602.27 -	612.00	344.08	12/2021 -	03/2020
	<u>Rail Vikas Nigam Ltd.</u>						
15	BHANUPALI-BILASPUR BERI NL - [N22000273]	4/2008	2,966.99 -	7,000.00	472.83	12/2026 -	12/2025
16	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78 -	723.78	0.19	12/2025 -	03/2025
	Total		10,501.06 -	14,493.48	2,649.03		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
17	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) [N24000415]	8/2010	195.04 -	377.99	312.41	10/2010 12/2020	06/2020
18	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]	1/2017	576.48 -	576.48	237.30	01/2018 12/2020	01/2020
	<u>National Highways Authority Of India</u>						
19	GWALIOR-JHANSI, NH-75 - [N24000089]	12/2003	604.00 364.59	364.59	237.64	12/2009 08/2020	03/2020
20	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]	3/2017	247.02 -	157.49	31.97	03/2020 02/2021	02/2020
	Total		1,622.54 -	1,476.55	819.32		
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
21	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]	10/2016	422.00 -	422.00	15.11	- 03/2021	12/2020
22	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]	11/2017	171.72	171.72	45.00	03/2020 11/2020	03/2020
	Total		593.72 -	593.72	60.11		
	Grand Total		34,673.81	43,950.11	23,050.31		

List of Projects on schedule w.r.t. Latest Schedule

Annexure - XII

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
1	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]	8/2018	951.28 -	951.28	71.55	10/2021 -	10/2021
2	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]	6/2018	1,383.00 -	1,383.00	210.62	09/2021 -	09/2021
3	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	7/2018	323.19 -	323.19	10.14	09/2021 -	09/2021
4	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082]	5/2018	539.20 -	539.20	25.64	10/2022 -	10/2022
5	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA - [N04000081]	1/2019	264.99 -	264.99	.42	11/2021 -	11/2021
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT - [N04000079]	3/2017	358.89 -	358.89	29.73	04/2021 -	04/2021
7	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]	12/2016	859.86 -	860.00	232.44	03/2021 -	03/2021
8	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN - [N04000085]	7/2018	353.27 -	353.27	114.29	09/2020 -	09/2020
	Total		5,033.68 -	5,033.82	694.83		
	<u>COAL</u>						
	<u>Bharat Coking Coal Limited</u>						
9	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	5.38	03/2021 -	03/2021
10	MOONIDIH XV SEAM UG - [N06000098]	8/2011	1,230.27 -	1,230.27	414.42	04/2015 04/2022	04/2022
	<u>Central Coal Fields Limited</u>						
11	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	190.41	03/2020 -	03/2020
12	NORTH URIMARI EXPANSION OCP - [N06000182]	3/2019	1,553.06 -	1,553.06	204.04	03/2023 -	03/2023
	<u>Eastern Coal Fields Limited</u>						
13	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	318.97	03/2022 -	03/2022
14	SIDULI MINE (OC AND UG) - [N06000165]	5/2018	535.18 -	535.18	.19	03/2026 -	03/2026

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
15	CHITRA EAST (RCE) OCP - [N06000169]	8/2018	513.98 -	513.98	93.85	03/2024 -	03/2024
16	PARASEA- BELBAID REORGANISATION UG MINE - [N06000185]	7/2019	826.42 -	826.42	-	03/2027 -	03/2027
17	NAKRAKONDA KUMARDIH B OCP - [N06000170]	8/2018	502.68 -	502.68	-	03/2029 -	03/2029
18	TILABONI UG MINE - [N06000172]	2/2019	916.62 -	916.62	-	03/2027 -	03/2027
19	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	112.11	03/2022 -	03/2022
	<u>Mahanadi Coal Fields Limited</u>						
20	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	1,213.54	03/2026 -	03/2026
21	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]	11/2018	2,838.87 -	2,838.87	1,169.40	03/2029 -	03/2029
22	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]	5/2018	2,434.75 -	2,434.75	140.36	03/2027 -	03/2027
23	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	445.23	03/2021 -	03/2021
	<u>Neyveli Lignite Corporation</u>						
24	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	8,596.47	11/2021 -	11/2021
	<u>Northern Coal Fields Limited</u>						
25	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]	5/2017	1,783.09 -	1,783.09	292.75	03/2021 -	03/2021
26	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]	11/2017	1,255.17 -	1,255.17	123.08	03/2022 -	03/2022
27	BLOCK-B EXPANSION OPENCAST PROJECT - [N06000184]	7/2019	998.71 -	998.71	-	03/2023 -	03/2023
28	SEMARIA OPENCAST PROJECT - [N06000176]	5/2019	396.58 -	396.58	-	03/2026 -	03/2026
	<u>Singareni Colliers Company Limited</u>						
29	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]	12/2015	477.65 -	477.65	2.11	03/2020 -	03/2020
	<u>South-Eastern Coal Fields Limited</u>						
30	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	9/2008	152.43 -	459.49	195.34	03/2015 03/2020	03/2020
31	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	6.58	03/2023 -	03/2023
32	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
33	MALACHUA OPENCAST PROJECT - [N06000139]	10/2015	488.33 -	488.33	27.33	03/2023 -	03/2023
34	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	110.31	03/2022 -	03/2022
35	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	2,358.32	03/2023 -	03/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
36	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	4.94	03/2023 -	03/2023
37	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	88.82	03/2020 -	03/2020
38	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
39	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	48.13	03/2021 -	03/2021
40	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	104.77	03/2021 -	03/2021
41	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
42	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	81.59	03/2020 -	03/2020
43	JHIRIA WEST OPENCAST PROJECT - [N06000166]	11/2018	389.97 -	389.97	-	03/2026 -	03/2026
44	MAHAMAYA OPENCAST PROJECT - [N06000164]	5/2018	410.26 -	410.26	9.53	03/2026 -	03/2026
45	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	75.96	03/2026 -	03/2026
46	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]	3/2016	869.44 -	869.44	117.99	03/2021 -	03/2021
	<u>Western Coal Fields Limited</u>						
47	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	202.03	03/2020 -	03/2020
48	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	263.81	03/2025 -	03/2025
49	BHANEAGAON OC - [N06000121]	2/2015	187.94 -	409.68	129.61	03/2023 -	03/2023
50	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	218.63	03/2020 -	03/2020
51	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	120.69	03/2020 -	03/2020
52	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	225.02	03/2021 -	03/2021
53	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	415.50	03/2020 -	03/2020
54	BELLORA-NAIGAON DEEP OC - [N06000180]	11/2018	252.71 -	252.71	58.07	03/2021 -	03/2021
55	UKNI DEEP OC - [N06000179]	11/2018	318.14 -	318.14	148.14	03/2021 -	03/2021
56	VISHNUPURI UG TO OC MINE - [N06000178]	7/2018	195.57 -	195.57	2.94	03/2025 -	03/2025
57	SAONER I UG TO OC PHASE I - [N06000177]	11/2016	162.10 -	162.10	51.16	03/2022 -	03/2022
58	KOLAR PIMPRI EXTENSION OC - [N06000160]	3/2017	362.73 -	362.73	322.62	03/2020 -	03/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
59	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]	2/2017	328.00 -	328.00	186.61	03/2021 -	03/2021
60	DHANKASA UG (1.00 MTY) - [N06000155]	9/2016	458.07 -	458.07	22.46	03/2022 -	03/2022
61	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	319.76	190.69	03/2022 -	03/2022
62	GANDHIGRAM UG MINE - [N06000183]	8/2019	414.16 -	414.16	.50	03/2026 -	03/2026
63	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]	7/2016	409.87 -	409.87	19.96	03/2022 -	03/2022
	Total		65,234.30 -	65,763.90	19,130.36		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Central Public Works Department</u>						
64	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR - [N21000029]	3/2019	1,404.00 -	1,404.00	-	09/2023 -	09/2023
65	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]	3/2019	1,577.00 -	1,828.00	-	09/2025 -	09/2025
	<u>National Building Construcion Corporation Ltd</u>						
66	AIIMS BILASPUR - [N21000028]	4/2018	1,351.00 -	1,471.00	421.44	09/2021 -	09/2021
	Total		4,332.00 -	4,703.00	421.44		
	<u>HUMAN RESOURCE DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
67	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA. - [N42000002]	5/2019	303.90 -	303.90	-	03/2020 -	03/2020
	Total		303.90 -	303.90	.00		
	<u>MINES</u>						
	<u>National Aluminum Company Limited (Nalco)</u>						
68	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	5,540.00 -	5,540.00	131.22	04/2021 12/2022	12/2022
69	UTKAL D AND E COAL BLOCK - [N10000011]	5/2016	534.00 -	534.00	320.63	01/2020 -	01/2020
70	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]	12/2015	355.00 -	355.00	85.98	11/2020 -	11/2020
71	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]	9/2017	166.62 -	163.17	135.00	06/2019 12/2020	12/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
72	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]	11/2017	483.00 -	483.00	.48	04/2021 04/2021	04/2021
	Total		7,078.62 -	7,075.17	673.31		
	PETROLEUM						
	Bharat Petroleum Corporation Limited						
73	HALDIA LPG IMPORT FACILITY - [N16000223]	3/2015	694.00 -	1,097.54	856.34	10/2018 02/2020	02/2020
74	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]	2/2016	554.00 -	554.00	375.80	02/2020 -	02/2020
75	2ND GENERATION LIGNOCELLULOSE BIOMASS ETHANOL BIOFUEL REFINERY AT BARGARH (ODISHA) - [N16000374]	8/2019	1,607.00 -	1,607.00	40.99	08/2022 -	08/2022
76	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]	11/2018	248.55 -	248.55	29.20	06/2022 -	06/2022
77	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL - [N16000365]	12/2017	1,524.06 -	1,524.06	22.01	12/2021 -	12/2021
78	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364]	7/2017	580.20 -	580.20	66.56	02/2021 -	02/2021
79	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]	10/2018	206.26 -	206.26	13.42	03/2021 -	03/2021
80	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]	9/2018	11,130.00 -	11,130.00	89.09	03/2023 -	03/2023
81	2G ETHANOL BIO REFINERY AT BARGARH - [N16000341]	8/2017	750.00 -	750.00	34.73	12/2020 -	12/2020
82	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]	12/2015	1,112.00 -	1,507.24	566.00	06/2019 02/2022	02/2022
83	PUNE POL STORAGE DEPOT - [N16000313]	8/2016	282.64 -	282.64	164.77	08/2020 -	08/2020
84	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]	2/2016	3,313.00 -	3,288.96	1,673.55	02/2020 10/2020	10/2020
85	MMPL PIPELINE REROUTING PROJECT - [N16000261]	4/2013	449.58 -	449.58	215.10	12/2019 07/2020	07/2020
	Gas Authority Of India Limited						
86	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	2/2015	749.00 -	842.00	606.89	02/2020 -	02/2020
87	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	3/2017	1,933.00 -	1,933.00	1,068.40	12/2020 -	12/2020
88	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]	3/2017	3,437.00 -	3,437.00	1,326.48	12/2020 -	12/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
89	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	3/2017	1,740.00 -	1,740.00	612.62	12/2020 -	12/2020
90	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	287.49	138.25	04/2022 -	04/2022
91	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR [N16000289]	7/2017	243.53 -	243.53	58.94	07/2022 -	07/2022
92	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]	8/2018	286.42 -	286.42	6.18	08/2020 09/2020	09/2020
93	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]	9/2018	225.54 -	225.54	2.44	02/2021 -	02/2021
94	BARAUNI-GUWAHATI PIPELINE - [N16000334]	6/2018	3,308.00 -	3,308.00	1,433.56	12/2021 -	12/2021
95	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR [N16000330]	10/2017	221.45 -	221.45	52.67	10/2022 -	10/2022
96	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329]	10/2017	226.45 -	226.45	62.72	10/2022 -	10/2022
97	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]	7/2017	182.20 -	182.20	34.88	07/2022 -	07/2022
98	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]	10/2017	359.25 -	359.25	81.40	10/2022 -	10/2022
99	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II [N16000285]	6/2009	2,915.00 2,915.00	4,915.00	2,784.58	12/2012 02/2022	02/2022
100	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]	3/2017	2,433.00 -	2,433.00	1,566.59	12/2020 -	12/2020
101	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]	7/2015	2,881.40 -	2,000.00	1,326.88	12/2020 -	12/2020
Hindustan Petroleum Corporation Limited							
102	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,928.00 -	26,264.00	8,584.07	07/2020 07/2022	07/2022
103	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA [N16000312]	11/2017	255.00 -	255.00	128.36	11/2020 -	11/2020
104	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE [N16000369]	12/2018	854.00 -	854.00	56.18	12/2022 -	12/2022
105	SETTING UP OF PHASE LL FACILITIES FOR HPCL GREEN R AND D CENTRE AT BENGALURU - [N16000380]	6/2018	380.00 -	380.00	82.70	11/2021 -	11/2021
106	SWRO II WITH LLPH FACILITIES - [N16000378]	9/2019	196.26 -	196.26	-	07/2020 -	07/2020
107	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367]	6/2019	2,166.38 -	2,166.38	33.41	06/2022 -	06/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
108	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]	9/2016	1,879.00 -	1,879.00	1,590.22	06/2020 -	06/2020
109	EXTENSION OF VISAKH-VIJAYAWADA- SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	9/2017	2,677.00 -	2,677.00	1,106.90	03/2021 -	03/2021
110	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]	9/2015	4,199.00 -	5,060.00	3,446.40	03/2020 -	03/2020
	<u>Indian Oil Corporation Limited</u>						
111	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]	5/2013	711.00 -	711.00	11.12	06/2020 -	06/2020
112	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]	7/2018	189.00 -	189.00	33.25	01/2021 -	01/2021
113	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]	3/2018	676.00 -	676.00	271.05	12/2021 -	12/2021
114	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]	12/2017	199.36 -	199.36	9.39	10/2020 -	10/2020
115	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]	8/2017	255.40 -	255.40	6.53	08/2020 -	08/2020
116	LPG BP PROJECT MOTIHARI - [N16000317]	5/2018	206.50 -	206.50	38.09	03/2021 -	03/2021
117	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309]	8/2017	1,342.00 -	1,342.00	6.30	08/2020 -	08/2020
118	AUGMENTATION OF CTMPL - [N16000286]	12/2016	228.00 -	228.00	36.09	06/2020 -	06/2020
119	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]	9/2016	208.35 -	208.35	148.25	07/2020 -	07/2020
120	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]	5/2016	261.00 -	261.00	71.13	01/2021 -	01/2021
121	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383]	9/2019	164.69 -	164.69	-	07/2021 -	07/2021
122	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY - [N16000382]	11/2019	5,251.00 -	5,251.00	-	05/2023 -	05/2023
123	LPG BP PROJECT CHITTOOR - [N16000381]	7/2019	167.00 -	167.00	3.62	07/2022 -	07/2022
124	LAB REVAMP AT GUJARAT REFINERY - [N16000377]	10/2019	403.00 -	403.00	43.50	12/2021 -	12/2021
125	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]	8/2019	1,255.00 -	1,255.00	106.50	10/2021 -	10/2021
126	R and D CAMPUS II AT FARIDABAD - [N16000375]	6/2019	2,281.94 -	2,281.94	-	12/2022 -	12/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
127	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]	6/2019	371.00 -	371.00	-	09/2022 -	09/2022
128	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT - [N16000363]	12/2018	278.60 -	278.60	-	06/2021 -	06/2021
129	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]	5/2019	3,361.00 -	3,361.00	468.48	08/2021 -	08/2021
130	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]	11/2018	462.30 -	462.30	-	09/2021 -	09/2021
131	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP [N16000350]	10/2018	316.20 -	316.20	18.83	10/2021 -	10/2021
132	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]	10/2018	1,297.50 -	1,297.50	30.00	10/2021 -	10/2021
133	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]	4/2018	522.00 -	522.00	187.36	03/2021 -	03/2021
134	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]	8/2018	1,636.00 -	1,636.00	160.86	08/2020 -	08/2020
135	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]	4/2018	5,654.00 -	5,654.00	686.68	10/2021 -	10/2021
136	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM [N16000270]	7/2014	247.00 -	247.00	-	03/2021 -	03/2021
137	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]	1/2015	342.00 -	342.00	-	03/2021 -	03/2021
138	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]	4/2016	1,021.00 -	1,021.00	4.45	12/2020 -	12/2020
139	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	1,074.02	08/2021 -	08/2021
140	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	1/2015	1,823.00 -	3,027.90	1,030.43	12/2020 -	12/2020
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
141	SEA WATER DESALINATION PLANT - [N16000319]	11/2017	581.00 -	621.00	154.66	03/2020 11/2020	11/2020
	<u>Numaligarh Refinery Limited</u>						
142	NUMALIGARH REFINERY EXPANSION PROJECT - [N16000379]	1/2019	22,594.00 -	22,594.00	43.00	10/2024 -	10/2024
	<u>Oil & Natural Gas Corporation Limited</u>						
143	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]	11/2014	6,068.80 -	5,296.93	4,845.91	04/2019 03/2020	03/2020
144	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	3/2011	861.79 -	1,683.06	1,386.15	05/2013 02/2020	02/2020
145	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]	5/2019	763.92 -	763.92	205.99	12/2020 -	12/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
146	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]	4/2019	3,228.80 -	3,228.80	510.66	03/2022 -	03/2022
147	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]	2/2019	2,292.46 -	2,292.46	815.60	05/2021 -	05/2021
148	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) - [N16000335]	4/2018	766.37 -	766.37	481.94	12/2019 03/2020	03/2020
149	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]	2/2017	4,006.83 -	4,475.92	2,975.26	05/2021 12/2021	12/2021
150	DEVELOPMENT OF B-147 FIELD - [N16000292]	2/2017	546.15 -	565.15	468.71	11/2019 03/2020	03/2020
151	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	1,162.56	441.61	03/2026 -	03/2026
152	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	7/2016	249.85 250.00	265.49	152.67	05/2020 -	05/2020
153	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]	1/2015	4,619.94 -	4,619.94	4,586.11	12/2017 03/2020	03/2020
154	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	823.27 -	910.23	441.81	03/2023 03/2022	03/2022
155	Field Development Plan of Madanam NLP-IV Block CY-ONN-2002 - [N16000241]	11/2015	650.82 -	650.82	432.28	03/2019 05/2020	05/2020
156	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	2,369.08	04/2018 05/2020	05/2020
157	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	1,933.09	03/2015 03/2020	03/2020
158	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]	8/2015	2,818.88 -	2,818.88	2,401.67	03/2019 05/2020	05/2020
159	DAMAN DEVELOPMENT PROJECT - [N16000198]	8/2014	6,086.08 -	5,842.31	4,784.88	05/2019 03/2020	03/2020
	<u>Oil India Limited</u>						
160	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	7/2011	352.56 -	438.84	268.45	03/2017 06/2020	06/2020
161	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN - [N16000356]	6/2016	224.75 -	224.75	98.98	08/2020 -	08/2020
162	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]	9/2016	571.66 -	571.66	372.70	12/2019 06/2020	06/2020
163	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]	5/2016	406.00 -	406.00	106.50	10/2020 -	10/2020
	Total		1,75,417.31 -	1,85,990.67	65,062.92		

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>POWER</u>						
	<u>National Hydro-Electric Power Corporation</u>						
164	PARBATI HEP (4X200 MW) (NHPC) II - [N180100210]	9/2002	3,919.59 -	9,997.11	7,761.19	09/2009 12/2021	12/2021
165	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [N180100221]	9/2003	6,285.33 -	19,496.34	11,842.12	09/2010 08/2023	08/2023
	<u>National Thermal Power Corporation</u>						
166	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	12,865.92	12,503.29	01/2018 03/2020	03/2020
167	PATRATU STPP-I (3X800MW) - [N18000275]	11/2017	18,668.00 -	18,668.00	2,409.34	03/2023 -	03/2023
168	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000274]	3/2019	349.00 -	349.00	125.00	11/2020 -	11/2020
169	BARH STPP(3X660MW) NTPC - [N180100242]	2/2005	8,692.97 -	21,312.11	16,928.07	10/2011 08/2021	08/2021
170	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	12,826.56	10/2017 03/2020	03/2020
171	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000273]	12/2018	587.44 -	587.44	250.00	09/2020 -	09/2020
172	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]	4/2012	9,750.89 -	12,176.28	10,103.00	02/2017 06/2020	06/2020
	<u>North East Electric Power Corporation</u>						
173	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [N180100239]	12/2004	2,496.90 -	7,927.34	7,743.76	12/2009 06/2020	06/2020
	<u>Power Grid Corporation Of India Limited</u>						
174	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	2/2009	11,130.19 -	14,719.10	12,824.45	08/2013 03/2022	03/2022
175	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPG AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]	12/2017	193.14 -	193.14	102.44	06/2019 03/2020	03/2020
176	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]	11/2017	358.83 -	358.83	177.36	05/2020 -	05/2020
177	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) [N18000267]	9/2017	198.49 -	198.49	126.26	09/2019 02/2020	02/2020
178	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]	5/2017	175.64 -	175.64	106.20	09/2018 03/2020	03/2020
179	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	3/2017	3,500.00 3,500.00	3,500.00	2,039.35	07/2020 -	07/2020
180	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]	2/2017	5,070.13 -	5,070.13	3,270.48	04/2020 -	04/2020
181	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]	4/2016	454.11 -	454.11	297.68	04/2018 01/2020	01/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
182	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]	3/2016	808.63 -	808.63	547.80	01/2018 03/2020	03/2020
	<u>Satluj Jal Vidyut Nigam Limited</u>						
183	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]	3/2019	10,439.09 -	10,439.09	876.79	01/2024 -	01/2024
184	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	648.33	310.91	12/2021 -	12/2021
	<u>Thdc India Limited</u>						
185	AMELIA COAL MINE - [N18000252]	1/2017	2,104.21 -	1,587.16	309.90	09/2020 -	09/2020
186	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]	3/2019	11,089.42 -	11,089.42	909.73	09/2023 -	09/2023
	Total		1,20,404.88 -	1,65,361.43	1,04,391.68		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
187	WARDHA-NANDED MAHARASHTRA - [N22000231]	4/2008	3,168.29 -	3,168.29	1,268.08	03/2023 -	03/2023
188	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]	2/2016	9,968.00 -	9,968.00	-	03/2024 -	03/2024
189	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	4/2011	184.06 -	312.00	293.06	03/2019 03/2020	03/2020
190	PUNE-NASIK (265 KM) - [N22000354]	2/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024
191	DAUND - MANMAD (236 KM) - [N22000360]	2/2016	1,876.00 -	2,081.27	230.40	03/2023 -	03/2023
192	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]	2/2015	2,449.91 -	2,449.91	218.30	03/2023 -	03/2023
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
193	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	03/2020
	<u>East Central Railways</u>						
194	KOSI BRIDGE (NL), ECR - [220100304]	4/2002	499.41 -	516.02	404.10	03/2020 -	03/2020
195	ARARIA-SUPAUL (NL) - [N22000177]	4/2008	1,605.17 -	1,605.17	23.55	- 03/2023	03/2023
	<u>East Coast Railway</u>						
196	SAMBALPUR-TALCHER DOUBLING - [N22000315]	3/2011	1,111.99 -	1,539.28	972.93	02/2019 03/2022	03/2022
197	BHADRAK - NERGUNDI 3RD LINE - [N22000316]	3/2013	843.04 -	843.04	147.39	10/2020 03/2023	03/2023
198	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,160.83	749.76	03/2020 03/2023	03/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
199	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]	4/2015	2,499.71 -	3,382.95	447.56	03/2022 03/2024	03/2024
200	JAGADALPUR-KORAPUT DOUBLING - [N22000376]	4/2015	1,547.38 -	1,547.38	435.59	03/2022 03/2023	03/2023
	<u>North Central Railway</u>						
201	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	4/2015	668.70 668.00	680.00	330.00	03/2020 -	03/2020
202	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]	3/2018	4,329.53 -	4,329.53	3.90	03/2023 -	03/2023
203	JHANSI BINA DOUBLING - [N22000496]	9/2016	2,001.00 -	2,001.00	416.59	03/2021 -	03/2021
	<u>North East Frontier Railway</u>						
204	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	4/2008	2,393.47 -	5,021.45	3,183.01	03/2014 03/2022	03/2022
205	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	4/2008	333.76 -	360.00	6.74	- 03/2022	03/2022
206	DIMAPUR-TIZIT NL - [N22000196]	4/2013	4,274.00 -	4,274.00	-	03/2020 -	03/2020
207	AGARTALA-AKHAURA NL - [N22000195]	4/2012	569.63 -	670.00	82.81	03/2020 09/2021	09/2021
208	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	4/2010	221.42 -	380.00	38.18	- 03/2022	03/2022
209	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	4/2010	906.46 -	6,000.60	263.12	03/2021 -	03/2021
210	MURKONGSELEK-PASIGHAT NL - [N22000208]	4/2011	414.84 -	661.00	123.00	03/2020 -	03/2020
211	DIGARU-HOJAI (102 KM) - [N22000389]	4/2015	870.96 -	2,136.01	610.95	03/2021 -	03/2021
212	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	4/2010	242.22 -	471.00	69.09	03/2020 -	03/2020
	<u>North Eastern Railway</u>						
213	HATHUA-BHATNI (N L) (NER) - [220100319]	4/2005	230.03 -	230.03	277.14	12/2022 -	12/2022
214	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]	4/2016	600.00 -	600.00	69.85	01/2022 -	01/2022
215	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]	4/2016	1,900.00 -	1,277.06	-	01/2022 -	01/2022
216	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	3/2007	243.78 -	895.00	106.55	12/2021 -	12/2021
	<u>Northern Railway</u>						
217	CHANDIGARH-BADDI - [N22000467]	4/2007	328.14 -	1,540.00	234.79	03/2023 -	03/2023
	<u>National High Speed Rail Corporation Limited</u>						
218	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]	12/2015	1,08,000.00 -	1,08,000.00	6,708.69	12/2023 12/2023	12/2023
	<u>Rail India Technical And Economic Service</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
219	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	392.54	03/2021 -	03/2021
220	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498]	2/2016	393.98 -	393.98	290.45	03/2020 -	03/2020
	<u>Rail Vikas Nigam Ltd.</u>						
221	AHMEDABAD-BOTAD (GC) - [N22000140]	4/2012	975.62 -	1,082.32	1,202.24	12/2021 -	12/2021
222	VIJAYAWADA-GUDUR - [N22000369]	4/2015	3,246.26 -	3,548.67	1,384.54	12/2023 -	12/2023
223	DHASA-JETALSAR (GC) - [N22000141]	4/2012	644.38 -	644.38	507.11	03/2021 -	03/2021
224	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	1/1991	2,335.67 -	2,335.68	698.45	12/2024 -	12/2024
225	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	773.94 -	773.94	556.16	12/2024 -	12/2024
	<u>South Central Railway</u>						
226	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	4/2010	704.31 -	927.94	303.24	03/2020 03/2020	03/2020
	<u>South East Central Railway</u>						
227	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	4/2005	383.79 -	1,413.76	1,351.73	- 01/2020	01/2020
228	ANUPPUR-KATNI - [N22000485]	4/2015	1,370.00 -	1,370.94	332.76	12/2021 03/2023	03/2023
229	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	4/2015	1,973.00 -	1,973.64	185.98	03/2021 03/2023	03/2023
230	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]	4/2008	872.00 -	1,226.51	1,066.54	12/2019 03/2020	03/2020
231	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	6/2018	229.00 -	852.50	39.69	12/2021 03/2023	03/2023
232	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]	4/2010	585.93 -	1,268.32	687.95	02/2019 12/2020	12/2020
233	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	9/2016	1,908.51 -	2,686.63	540.55	03/2023 03/2023	03/2023
234	GONDIA-JABALPUR(GC),(SECR) - [220100186]	2/1997	511.86 -	1,756.00	1,679.29	04/2020 01/2021	01/2021
	<u>South Eastern Railway</u>						
235	BOWAICHANDI-ARAMBAGH - [N22000159]	4/2010	267.37 -	620.00	40.99	- 03/2025	03/2025
236	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	4/1998	1,027.40 -	2,373.00	485.04	03/2003 03/2030	03/2030
237	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	4/2010	651.00 -	1,009.00	7.96	03/2015 03/2025	03/2025
	<u>South Western Railway</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
238	YELAHANKA-PENUKONDA - [N22000328]	5/2015	860.43 -	958.00	781.04	03/2020 -	03/2020
239	ARSIKERE-TUMKUR - [N22000332]	3/2015	578.00 -	578.00	565.04	03/2020 -	03/2020
	<u>Southern Railway</u>						
240	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]	2/2015	1,700.00 -	1,003.00	252.02	03/2022 -	03/2022
	<u>Western Railway</u>						
241	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	4/2008	3,503.69 -	3,975.22	1,801.98	03/2022 03/2023	03/2023
242	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	4/2008	318.24 -	321.62	125.76	03/2012 03/2022	03/2022
243	CHOTTAUDEPUR-DHAR(NL) - [N22000138]	4/2007	1,347.26 -	1,347.26	756.98	03/2022 03/2022	03/2022
244	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	4/2008	829.74 -	1,310.23	1,532.69	03/2020 03/2021	03/2021
245	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]	4/2007	1,640.04 -	1,640.04	756.11	03/2022 03/2023	03/2023
246	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]	4/2017	691.84 -	663.29	199.24	03/2020 03/2021	03/2021
247	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]	4/2016	700.00 -	603.69	146.09	06/2020 06/2021	06/2021
248	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]	2/1991	551.51 -	809.07	635.52	03/2019 03/2020	03/2020
249	SURENDRA NAGAR RAJKOT - [N22000392]	4/2015	1,002.39 -	1,002.39	454.02	03/2021 03/2021	03/2021
250	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	4/2011	1,037.15 -	1,037.15	1,035.89	03/2021 03/2022	03/2022
251	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	4/1994	320.66 -	858.96	534.00	03/2019 03/2022	03/2022
252	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]	4/2011	844.10 -	844.10	110.71	- 03/2021	03/2021
	Total		2,09,873.35 -	2,68,389.11	61,640.43		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
253	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]	3/2015	271.45 -	271.45	182.45	10/2015 01/2020	01/2020
254	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]	2/2018	206.13 -	206.13	127.86	06/2020 -	06/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
255	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987	1/2018	283.15 -	283.15	42.22	05/2020 -	05/2020
256	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969	1/2017	263.45 -	263.45	60.26	09/2017 12/2020	12/2020
257	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968	11/2016	376.25 -	376.25	228.69	08/2017 02/2020	02/2020
258	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966	1/2016	348.95 -	348.95	169.46	08/2016 03/2020	03/2020
259	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967	3/2016	444.84 -	444.84	273.88	09/2016 03/2020	03/2020
260	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964	8/2016	350.61 -	350.61	310.25	01/2017 04/2020	04/2020
261	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963	1/2018	418.03 -	418.03	194.62	08/2018 08/2020	08/2020
262	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941	3/2018	293.64 -	293.64	134.32	08/2020 -	08/2020
263	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 KM - [N24001230	11/2018	281.45 -	281.45	2.36	12/2020 -	12/2020
264	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I - [N24001216	12/2016	196.00 -	196.00	-	09/2021 -	09/2021
265	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209	3/2016	296.50 -	296.50	74.77	09/2020 -	09/2020
266	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208	3/2018	288.30 -	288.30	41.74	08/2020 -	08/2020
267	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207	3/2018	185.18 -	185.18	79.93	02/2020 -	02/2020
268	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206	3/2018	263.89 -	242.05	139.94	04/2020 -	04/2020
269	R AND U FROM KM 385.00 TO KM 420.000 TO 2- LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404 - [N24001205	12/2016	209.10 -	209.10	160.28	10/2019 04/2020	04/2020
270	REHABILITATION AND UPGRADATION OF ALLAHABAD - MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203	10/2016	218.90 -	218.90	64.59	03/2020 -	03/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
271	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]	1/2019	264.50 -	264.50	-	03/2021 -	03/2021
272	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197]	3/2018	351.00 -	351.00	.49	06/2021 -	06/2021
273	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]	8/2010	186.96 -	305.61	279.13	09/2014 06/2020	06/2020
274	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180]	3/2019	237.51 -	237.51	-	12/2022 -	12/2022
275	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]	3/2017	217.35 -	217.35	35.10	11/2020 -	11/2020
276	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]	10/2016	171.90 -	171.90	23.19	08/2020 -	08/2020
277	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]	10/2016	172.63 -	172.63	77.30	12/2020 -	12/2020
278	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]	10/2016	167.62 -	167.62	61.37	12/2020 -	12/2020
279	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. - [N24001174]	10/2016	235.31 -	235.31	97.25	11/2020 -	11/2020
280	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152]	9/2018	160.00 -	160.00	.50	09/2021 -	09/2021
281	WARDHA TO ARVI - [N24001150]	2/2018	313.58 -	313.58	32.96	04/2020 -	04/2020
282	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148]	3/2016	599.34 -	599.34	492.15	01/2020 -	01/2020
283	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA - [N24001139]	10/2016	218.94 219.00	218.94	120.69	03/2020 -	03/2020
284	KALMATH TO ZARAP - [N24001137]	9/2016	1,338.13 1,338.00	1,338.13	959.51	03/2020 -	03/2020
285	TALGAON TO KALMATH - [N24001136]	10/2016	904.70 905.00	904.70	604.05	03/2020 -	03/2020
286	BHOGAN KHURD TO KASHEDI - [N24001132]	9/2017	743.21 743.00	743.21	131.87	06/2021 -	06/2021
287	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131]	3/2018	212.99 -	212.99	99.21	06/2020 -	06/2020
288	BAMNI TO NAVAEGAON - [N24001110]	9/2017	241.69 242.00	241.69	109.29	04/2020 -	04/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
289	PANCHARAL TO MANDANGHAR - [N24001107	7/2018	381.08 302.00	381.08	13.03	05/2020 -	05/2020
290	SELDOH TO PANVAR - [N24001097	7/2018	404.33 404.00	404.33	44.19	05/2020 -	05/2020
291	PAHUR TO BODHWAD - [N24001084	1/2017	244.93 -	244.93	75.23	05/2020 -	05/2020
292	ARDHAPUR TO HIMAYATNAGAR - [N24001079	12/2017	426.06 426.00	426.06	91.97	06/2020 -	06/2020
293	OSMANNAGAR TO KUNDRAL - [N24001075	9/2017	344.25 344.00	344.25	71.18	08/2020 -	08/2020
294	KOTHARI TO DHANORA - [N24001073	9/2018	301.38 301.00	301.38	59.42	08/2020 -	08/2020
295	JALKOT TO TOGRI - [N24001071	7/2018	299.92 300.00	299.92	19.25	08/2020 -	08/2020
296	DHANGIPIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK [N24001064	3/2018	217.14 217.00	217.14	100.77	02/2020 -	02/2020
297	WADIGODRI TO DHANGRIPIMPRI - [N24001063	3/2018	194.23 194.00	194.23	88.23	02/2020 -	02/2020
298	NILAJPHATA TO BHANDARA - [N24001043	1/2018	420.63 421.00	420.63	50.60	05/2020 -	05/2020
299	MAHAD TO RAIGAD FORT - [N24001038	7/2018	237.40 -	237.40	8.34	05/2020 -	05/2020
300	PATRADEVI TO KARASWADA 4L - [N24001004	3/2017	634.32 -	634.32	109.33	05/2020 -	05/2020
301	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994	3/2018	626.76 -	626.76	80.66	07/2020 -	07/2020
302	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993	3/2018	322.81 -	322.81	1.66	09/2020 -	09/2020
303	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992	2/2018	426.52 -	426.52	225.51	04/2020 -	04/2020
304	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940	3/2016	995.09 995.00	995.09	419.22	05/2016 07/2020	07/2020
305	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939	3/2018	504.19 504.00	504.19	248.37	11/2018 05/2020	05/2020
306	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938	3/2018	297.12 294.00	294.12	373.98	07/2018 01/2020	01/2020
307	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937	3/2018	289.67 290.00	289.67	105.02	08/2018 02/2020	02/2020
308	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU - [N24000936	3/2018	244.95 245.00	244.95	136.22	08/2018 02/2020	02/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
309	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934	3/2018	228.32 -	228.32	48.15	08/2018 03/2020	03/2020
310	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933	2/2017	429.43 -	429.43	255.68	11/2017 03/2020	03/2020
311	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932	1/2017	319.28 -	319.28	111.98	08/2017 03/2020	03/2020
312	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931	11/2016	290.15 -	290.15	73.11	05/2017 03/2020	03/2020
313	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO - [N24000930	11/2016	378.24 -	378.24	307.17	01/2018 01/2020	01/2020
314	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH.0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928	10/2015	333.21 -	355.89	294.81	12/2015 01/2020	01/2020
315	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927	3/2018	293.64 -	293.64	28.24	08/2020 -	08/2020
316	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909	10/2017	1,069.59 -	1,069.59	663.50	10/2019 12/2020	12/2020
317	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907	3/2018	293.10 -	293.10	63.14	08/2020 -	08/2020
318	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906	3/2018	173.24 -	173.24	56.66	06/2020 -	06/2020
319	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905	3/2018	322.48 -	322.48	153.18	07/2020 -	07/2020
320	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781	5/2018	248.00 -	248.00	-	05/2020 -	05/2020
321	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306	11/2010	624.41 -	992.67	886.01	03/2011 12/2020	12/2020
322	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308	8/2010	193.69 -	327.92	258.71	10/2010 06/2021	06/2021
323	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904	1/2017	247.25 -	247.25	144.71	03/2019 06/2020	06/2020
324	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883	3/2018	254.30 -	254.30	53.46	10/2020 -	10/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
325	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]	2/2018	418.88 -	418.88	88.00	02/2020 -	02/2020
	<u>National Highways Authority Of India</u>						
326	KANDLA - MUNDRA PORT - [N24000175]	1/2011	953.88 -	953.88	976.79	07/2013 11/2020	11/2020
327	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]	12/2015	726.67 -	598.13	414.73	04/2018 03/2020	03/2020
328	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]	4/2017	894.00 -	929.32	760.00	04/2020 -	04/2020
329	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	3/2017	2,064.99 -	2,447.00	2,029.34	03/2020 06/2020	06/2020
330	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]	3/2017	239.68 -	235.90	91.24	03/2020 -	03/2020
331	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]	8/2016	1,664.20 -	1,664.20	794.87	04/2020 -	04/2020
332	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]	8/2016	1,388.34 -	2,587.50	1,449.00	09/2019 03/2020	03/2020
333	NAGPUR RING ROAD PACKAGE-2 - [N24000560]	3/2016	591.66 -	591.66	310.56	07/2019 12/2020	12/2020
334	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]	3/2016	720.00 -	720.00	343.72	- 10/2020	10/2020
335	NAGPUR RING ROAD PACKAGE-1 - [N24000558]	3/2016	546.00 -	546.00	269.67	07/2019 12/2020	12/2020
336	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]	3/2016	899.00 -	899.00	641.51	04/2019 07/2020	07/2020
337	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]	3/2016	229.37 -	229.37	112.94	11/2018 08/2020	08/2020
338	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]	10/2015	447.29 -	746.43	614.07	12/2017 06/2020	06/2020
339	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]	9/2015	414.51 -	414.00	543.46	05/2018 05/2020	05/2020
340	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]	3/2018	291.53 -	291.53	68.92	- 11/2020	11/2020
341	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]	3/2018	1,029.96 -	1,261.05	97.55	- 03/2021	03/2021
342	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]	3/2018	557.30 -	557.30	211.24	- 06/2020	06/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
343	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK - [N24000737]	1/2018	1,522.00 -	1,522.00	243.52	- 06/2021	06/2021
344	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]	3/2017	165.50 -	172.16	117.09	03/2020 -	03/2020
345	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]	3/2017	648.32 -	511.94	511.34	03/2020 -	03/2020
346	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	3/2017	672.89 -	736.01	-	03/2020 -	03/2020
347	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]	3/2017	639.79 -	552.90	578.15	03/2020 -	03/2020
348	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]	3/2017	296.19 -	254.00	254.85	03/2020 -	03/2020
349	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	3/2017	744.64 -	982.00	-	03/2020 -	03/2020
350	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]	3/2017	848.45 -	848.45	103.14	03/2020 -	03/2020
351	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]	11/2016	290.73 -	315.00	246.70	- 03/2020	03/2020
352	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]	12/2015	649.50 -	649.50	155.81	03/2019 04/2021	04/2021
353	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]	10/2015	593.26 -	636.24	490.35	05/2018 06/2020	06/2020
	Total		46,592.82 -	49,334.62	23,650.93		
	<u>SHIPPING AND PORTS</u>						
	<u>Inland Waterways Authority Of India</u>						
354	JAL MARG VIKAS PROJECT - [N25000072]	1/2018	4,200.00 -	5,369.18	1,540.69	03/2023 03/2023	03/2023
	Total		4,200.00 -	5,369.18	1,540.69		
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
355	NMDC INTEGRATED STEEL PLANT - [N12000086]	1/2010	15,525.00 -	23,140.00	16,468.33	05/2015 07/2020	07/2020
	<u>Rastriya Ispat Nigam Limited</u>						
356	FORGED WHEEL PLANT - [N12000116]	4/2014	1,682.85 -	1,682.85	1,341.85	09/2018 02/2020	02/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
357	COKE OVEN BATTERY-5 - [N12000117	12/2011	2,858.00 -	2,500.00	1,535.76	12/2017 03/2020	03/2020
358	CENTRAL DISPATCH YARD - [N12000119	8/2015	320.66 -	320.66	257.04	08/2018 02/2020	02/2020
	<u>Steel Authority Of India Limited (Sail)</u>						
359	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094	4/2015	3,127.30 -	3,127.30	3,201.42	04/2018 01/2020	01/2020
360	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095	3/2015	1,034.01 -	1,034.01	450.11	10/2017 06/2020	06/2020
361	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E - [N12000121	12/2018	263.36 -	263.36	29.03	09/2020 -	09/2020
	Total		24,811.18 -	32,068.18	23,283.54		
	<u>TELECOMMUNICATIONS</u>						
	<u>Bharat Sanchar Nigam Limited</u>						
362	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113	1/2018	231.80 -	240.10	119.92	10/2018 02/2020	02/2020
	Total		231.80 -	240.10	119.92		
	<u>URBAN DEVELOPMENT</u>						
	<u>Ahmedabad Metro Rail</u>						
363	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137	3/2019	5,384.17 -	5,384.17	4.35	03/2024 -	03/2024
364	SURAT METRO RAIL PROJECT - [N28000138	3/2019	12,020.32 -	12,020.32	4.67	03/2024 -	03/2024
	<u>Central Public Works Department</u>						
365	NSG AT KOLKATA - [N28000104	10/2014	162.88 -	162.88	148.52	04/2018 06/2020	06/2020
366	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI [N28000117	1/2018	223.37 -	223.37	48.89	07/2020 12/2020	12/2020
367	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118	10/2017	271.90 -	271.90	65.00	11/2019 08/2020	08/2020
368	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR [N28000126	1/2019	790.79 -	790.79	41.06	03/2022 06/2022	06/2022
369	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASपुरI NEW DELHI PHASE-I - [N28000128	10/2016	1,180.00 -	1,100.80	9.96	07/2021 -	07/2021
370	CONSTRUCTION OF GRAMEEN VIKAS BHAWAN (2BASEMENTS+ GROUND+9 FLOORS) FOR MINISTRY OF RURAL DEVELOPMENT - [N28000132	11/2018	361.60 -	361.60	.45	07/2021 -	07/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
371	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133]	2/2019	186.00 199.00	186.00	38.35	09/2020 -	09/2020
372	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]	10/2016	1,128.00 -	1,128.00	1.52	03/2022 -	03/2022
373	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]	12/2018	260.00 -	260.00	12.50	06/2021 -	06/2021
374	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]	11/2017	238.56 -	238.56	63.67	05/2020 -	05/2020
	<u>Chennai Metro Rail Ltd</u>						
375	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]	6/2016	3,770.00 -	3,770.00	2,258.91	03/2018 06/2020	06/2020
	<u>Delhi Metro Rail Corporation</u>						
376	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS - [N28000135]	7/2019	24,948.65 -	24,948.65	78.44	03/2025 -	03/2025
377	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136]	5/2017	565.00 -	565.00	420.66	12/2020 -	12/2020
	<u>Maharashtra Metro Rail Corporation Ltd.</u>						
378	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]	12/2016	11,420.00 -	11,420.00	3,614.06	11/2021 03/2022	03/2022
	<u>Madhya Pradesh Metro Rail Co Limited</u>						
379	BHOPAL METRO RAIL - [N28000124]	11/2018	6,941.40 -	6,941.40	58.37	02/2023 -	02/2023
380	INDORE METRO RAIL - [N28000125]	11/2018	7,500.80 -	7,500.80	54.74	02/2023 -	02/2023
	<u>National Capital Region Transport Corp</u>						
381	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134]	3/2019	30,274.00 -	30,274.00	690.64	06/2025 -	06/2025
	Total		1,07,627.44 -	1,07,548.24	7,614.76		
	<u>WATER RESOURCES</u>						
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>						
382	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026]	3/2018	230.06 -	230.06	-	07/2021 -	07/2021
383	SEWER NETWORKS, SPS AND STP, MUNGER - [N30000036]	3/2018	294.02 -	294.02	-	10/2021 -	10/2021
384	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR - [N30000038]	4/2015	184.93 -	184.93	163.36	04/2020 -	04/2020
385	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]	5/2017	356.37 -	356.37	66.44	04/2021 -	04/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
386	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]	5/2017	191.62 -	191.62	37.70	11/2020 -	11/2020
387	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA - [N30000051]	8/2017	824.00 -	824.00	.41	06/2022 -	06/2022
388	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]	8/2017	578.89 -	578.89	.29	06/2022 -	06/2022
389	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]	3/2017	277.42 -	277.42	85.87	05/2021 -	05/2021
390	SEWERAGE SCHEME AT PAHARI ZONE IVA S PATNA - [N30000041]	5/2017	184.86 -	184.86	103.13	05/2021 -	05/2021
391	SAIDPUR SEWER NETWORK PATNA - [N30000039]	4/2015	268.63 -	268.63	192.80	01/2021 -	01/2021
392	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]	12/2014	225.77 -	225.77	183.57	03/2020 -	03/2020
393	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]	3/2018	305.19 -	305.19	-	08/2021 -	08/2021
394	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]	10/2017	254.13 -	254.13	.05	09/2020 -	09/2020
395	I AND D AND STP AT CHAPPRA - [N30000028]	11/2018	236.15 -	236.15	.06	12/2020 -	12/2020
<u>Delhi Jal Board</u>							
396	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014]	3/2017	665.78 -	665.78	94.40	12/2022 -	12/2022
397	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018]	5/2017	344.81 -	344.81	-	05/2020 -	05/2020
398	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI - [N30000017]	12/2018	515.07 -	515.07	246.01	01/2021 -	01/2021
399	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015]	5/2016	211.79 -	211.79	39.14	12/2021 -	12/2021
400	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]	5/2016	239.11 -	239.11	42.77	02/2022 -	02/2022
<u>Kolkata Metropolitan Development Authority</u>							
401	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]	1/2019	384.96 -	384.96	-	04/2022 -	04/2022
402	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033]	3/2018	165.16 -	165.16	-	06/2022 -	06/2022
403	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH - [N30000042]	5/2018	160.00 -	160.00	-	02/2022 -	02/2022
404	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046]	2/2014	274.76 -	274.76	171.80	12/2019 02/2020	02/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
405	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI [N30000048]	1/2018	172.10 -	172.10	-	12/2021 -	12/2021
406	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]	10/2017	164.93 -	164.93	-	12/2021 -	12/2021
407	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE [N30000047]	12/2014	272.32 -	272.32	191.36	04/2020 -	04/2020
408	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]	8/2017	185.22 -	185.22	-	12/2021 -	12/2021
409	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA [N30000034]	8/2017	307.12 -	307.12	-	09/2022 -	09/2022
410	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA [N30000032]	5/2018	198.43 -	198.43	-	02/2022 -	02/2022
411	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPURL - [N30000030]	3/2019	287.53 -	287.53	-	04/2022 -	04/2022
412	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]	12/2018	234.31 -	234.31	-	04/2022 -	04/2022
	Uttar Pradesh Jal Nigam						
413	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006]	5/2017	767.59 -	767.59	.01	09/2021 -	09/2021
414	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010]	3/2018	967.23 -	967.23	-	09/2021 -	09/2021
415	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH [N30000025]	3/2019	298.12 -	298.12	-	07/2021 -	07/2021
416	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]	2/2019	681.78 -	681.78	-	06/2022 -	06/2022
417	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WORKS AT AGRA - [N30000023]	2/2019	317.19 -	317.19	-	08/2021 -	08/2021
418	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022]	1/2019	206.05 -	206.05	1.57	10/2021 -	10/2021
419	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH [N30000021]	1/2019	231.79 -	231.79	-	12/2021 -	12/2021
420	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA [N30000020]	2/2011	279.91 -	279.91	199.59	12/2019 03/2020	03/2020
421	MATHURA SEWERAGE SCHEME [N30000019]	12/2017	460.45 -	460.45	56.83	12/2020 -	12/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(January 2020)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
422	REHABILITATION RENOVATION OF AGRA SEWERAGE SCHEME INTERCEPTION AND DIVERSION WORKS IN AGRA UTTAR PR - [N30000012]	12/2018	857.26 -	857.26	-	08/2021 -	08/2021
423	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH - [N30000013]	3/2019	271.39 -	271.39	-	08/2021 -	08/2021
424	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA - [N30000011]	2/2017	161.31 -	161.31	37.60	11/2019 02/2020	02/2020
425	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR - [N30000009]	10/2016	370.40 -	370.40	268.59	08/2020 -	08/2020
426	INTEGRATED PROJECT FOR DEVELOPMENT OF STPS IN ALLAHABAD ALONG WITH EXISTING ASSETS - [N30000007]	3/2018	904.00 -	904.00	-	09/2021 -	09/2021
427	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]	10/2017	213.62 -	213.62	-	03/2022 -	03/2022
	<u>Uttarakhand Pey Jal Nigam</u>						
428	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI - [N30000003]	3/2017	273.37 -	273.37	53.19	08/2019 02/2020	02/2020
	Total		16,456.90 -	16,456.90	2,236.54		
	Grand Total		7,87,598.18	9,13,638.22	3,10,461.35		

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Annexure - XIII

Costing Rs. 150 Crore and above					(January 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 - 5,677.00	6,840.00	09/2010 -	10/2021	95.88
	<u>Nuclear Power Corporation Of India Limited</u>						
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 - 11,459.00	16,580.00	12/2015 -	09/2021	44.69
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]	10/2009	12,320.00 - 12,320.00	17,079.00	12/2016 -	03/2023	38.63
	Total		27,271.00 .00 29,456.00	40,499.00			
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	314.61 - 314.61	441.33	09/2018 -	06/2020	40.28
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI [N04000083]	12/2016	859.86 - 859.86	860.00	03/2021 -	03/2021	.02
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]	09/2015	338.93 - 338.93	339.00	06/2019 -	-	.02
	Total		1,513.40 .00 1,513.40	1,640.33			
	<u>COAL</u>						
	<u>Eastern Coal Fields Limited</u>						
7	RANIGANJ MASTER PLAN - [N06000163]	08/2009	2,661.73 - 2,661.73	5,146.48	08/2019 -	08/2024	93.35
	<u>Neyveli Lignite Corporation</u>						
8	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 - 17,237.00	17,237.80	11/2021 -	11/2021	.00
	<u>Singareni Colliers Company Limited</u>						

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(January 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
9	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 - 418.97	489.62	03/2012 -	03/2023	16.86
10	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 - 249.03	448.86	03/2012 -	03/2024	80.24
11	KAKATIYAKHANI OPENCASE-2 PROJECT - [N06000129]	05/2015	397.09 - 397.09	442.42	03/2019 -	03/2020	11.42
12	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 - 447.06	473.22	03/2015 -	03/2021	5.85
13	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 - 162.76	349.28	03/2015 -	03/2021	114.60
	<u>Western Coal Fields Limited</u>						
14	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 - 277.65	313.34	03/2021 -	03/2024	12.85
15	BHANEGAON OC - [N06000121]	02/2015	187.94 - 187.94	409.68	03/2023 -	03/2023	117.98
16	ADASA UG TO OC - [N06000133]	08/2015	288.90 - 288.90	333.43	03/2023 -	03/2024	15.41
	Total		22,328.13 .00 22,328.13	25,644.13			
	<u>COMMERCE AND INDUSTRY</u>						
	<u>India International Convention And Expo Centre</u>						
17	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]	11/2017	4,773.00 - 4,773.00	5,178.00	12/2019 -	09/2020	8.49
	Total		4,773.00 .00 4,773.00	5,178.00			
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Central Public Works Department</u>						
18	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]	03/2019	1,577.00 - 1,577.00	1,828.00	09/2025 -	09/2025	15.92
	<u>Hospital Services Consultancy Corporation Ltd</u>						
19	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	02/2013	414.11 - 414.11	499.23	11/2013 -	09/2020	20.55

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(January 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
20	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 - 204.44	270.00	05/2017 -	06/2020	32.07
21	AIIMS - OPD(NEW) - [N21000009]	08/2014	293.65 - 293.65	325.00	05/2017 -	01/2020	10.68
22	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]	12/2014	168.90 - 168.90	191.20	05/2017 -	07/2019	13.20
23	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	09/2014	505.58 - 505.58	585.00	03/2018 -	09/2019	15.71
24	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]	07/2016	152.95 - 152.95	177.92	02/2018 -	03/2020	16.33
25	CNCI KOLKATA WEST BENGAL - [N21000015]	08/2016	244.00 - 244.00	248.00	09/2018 -	05/2019	1.64
26	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS- MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	08/2017	272.19 - 272.19	272.54	03/2019 -	03/2020	.13
27	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]	12/2017	156.56 - 156.56	156.64	- -	05/2020	.05
28	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]	01/2018	249.01 - 249.01	249.07	- -	05/2020	.02
	Total		4,238.39 .00 4,238.39	4,802.60			
	<u>HUMAN RESOURCE DEVELOPMENT</u>						
	<u>Rail India Technical And Economic Service</u>						
29	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]	09/2013	484.32 - 484.32	626.26	09/2014 -	12/2020	29.31
	Total		484.32 .00 484.32	626.26			
	<u>PETROLEUM</u>						
	<u>Gas Authority Of India Limited</u>						
30	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	02/2015	749.00 - 749.00	842.00	02/2020 -	02/2020	12.42
	<u>Indian Oil Corporation Limited</u>						

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(January 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
31	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 - 607.06	714.25	10/2017 -	-	17.66
32	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL [N16000252]	05/2016	664.00 - 664.00	729.40	12/2020 -	02/2020	9.85
	<u>Indian Strategic Petroleum Reserves Ltd</u>						
33	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 - 993.00	1,693.00	01/2012 -	-	70.49
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
34	SEA WATER DESALINATION PLANT - [N16000319]	11/2017	581.00 - 581.00	621.00	03/2020 -	11/2020	6.88
	<u>Oil & Natural Gas Corporation Limited</u>						
35	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) [N16000128]	03/2011	861.79 - 861.79	1,683.06	05/2013 -	02/2020	95.30
36	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS [N16000213]	12/2015	3,190.69 - 3,190.69	3,247.19	04/2018 -	05/2020	1.77
37	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) [N16000297]	02/2017	4,006.83 - 4,006.83	4,475.92	05/2021 -	12/2021	11.71
	<u>Oil India Limited</u>						
38	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 - 352.56	438.84	03/2017 -	06/2020	24.47
39	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 - 871.35	1,200.00	03/2015 -	-	37.72
40	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	01/2018	543.91 - 543.91	682.90	02/2020 -	06/2020	25.55
	Total		13,421.19 .00 13,421.19	16,327.56			
	<u>POWER</u>						
	<u>National Hydro-Electric Power Corporation</u>						
41	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 - 3,919.59	9,997.11	09/2009 -	12/2021	155.06
42	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 - 6,285.33	19,496.34	09/2010 -	08/2023	210.19
	<u>National Thermal Power Corporation</u>						

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(January 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
43	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 - 11,638.55	12,865.92	01/2018 -	03/2020	10.55
44	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	09/2014	9,188.98 - 9,188.98	10,016.10	07/2019 -	09/2020	9.00
45	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 - 12,532.44	13,740.53	12/2018 -	08/2020	9.64
46	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 - 14,366.58	15,164.05	06/2019 -	03/2022	5.55
47	RAMMAM-III HEPP (3X40 MW) - [N18000178]	09/2014	1,381.84 - 1,381.84	1,592.34	09/2019 -	11/2022	15.23
48	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 - 7,998.00	9,583.00	07/2012 -	09/2020	79.02
49	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]	04/2012	9,750.89 - 9,750.89	12,176.28	02/2017 -	06/2020	24.87
50	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 - 11,846.00	12,739.82	10/2017 -	03/2020	7.55
51	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	07/2012	1,527.00 - 1,527.00	1,801.07	08/2017 -	-	17.95
52	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	03/2015	9,870.51 - 9,870.51	11,148.86	01/2020 -	02/2020	12.95
53	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00 4,238.00	4,552.00	10/2017 -	-	7.41
	<u>Power Grid Corporation Of India Limited</u>						
54	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 - 4,754.42	9,072.36	12/2018 -	12/2020	90.82
55	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 - 5,111.33	6,880.36	12/2018 -	12/2020	34.61
	<u>Thdc India Limited</u>						
56	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 - 2,491.58	4,397.80	06/2013 -	12/2022	76.51
	Total		1,14,256.00 4,238.00 1,16,901.04	1,55,223.94			

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(January 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
57	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89 -	1,377.48	03/2021 -	03/2022	73.73
58	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 -	312.00	03/2019 -	03/2020	69.51
59	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 -	4,517.49	03/2021 -	03/2022	98.88
60	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 -	5,341.68	03/2024 -	03/2024	120.28
61	VAIBHAVWADI-KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 -	3,438.51	03/2024 -	-	25.04
62	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	02/2015	3,627.47 -	3,627.47	03/2024 -	03/2023	.01
63	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	03/2023 -	03/2023	10.94
	<u>Container Corporation Of India</u>						
64	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 -	235.00	03/2019 -	12/2020	.21
	<u>East Central Railways</u>						
65	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	03/1999	1,033.07 -	3,376.00	- -	03/2021	226.79
66	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	324.73 -	1,050.00	03/2012 -	03/2020	223.35
67	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 -	549.75	- -	-	32.26
68	BIHTA-AURANGABAD (NL) - [N22000170]	04/2008	326.20 -	2,995.01	- -	03/2024	818.15
69	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	378.56 -	1,858.75	- -	03/2022	391.01
70	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	1,006.00	- -	-	376.78

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(January 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
71	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 - 367.17	440.00	- -	01/2020	106.56
72	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]	04/1991	329.39 - 803.11	1,483.14	- -	12/2021	350.27
	<u>East Coast Railway</u>						
73	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 - 198.07	1,928.07	06/2021 -	06/2024	137.80
74	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 - 155.81	238.03	03/2020 -	03/2021	52.77
75	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]	04/2015	2,499.71 - 2,499.71	3,382.95	03/2022 -	03/2024	35.33
76	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	04/2015	701.61 - 701.61	810.02	11/2018 -	03/2022	15.45
	<u>Eastern Railways</u>						
77	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 - 1,188.91	1,619.48	03/2019 12/2009	03/2025	36.22
78	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 - 607.09	1,425.44	02/2013 -	03/2024	134.80
79	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 - 365.17	527.54	- -	03/2025	44.46
80	HANSDIHA-GODDA NL - [N22000236]	04/2011	542.18 - 542.18	693.80	03/2020 -	03/2021	27.96
81	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]	04/2011	175.80 - 175.80	260.83	- -	03/2021	48.37
82	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	04/2011	299.60 - 299.60	335.62	03/2017 -	03/2026	12.02
83	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]	04/2010	494.54 - 494.54	494.59	03/2005 -	03/2025	.01
84	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]	04/2000	297.47 - 297.47	298.22	- -	03/2025	.25
85	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	499.96 - 499.96	680.68	02/2012 -	03/2025	36.15

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(January 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
86	MONIGRAM- NIMTITA - [N22000301]	04/2012	250.93 - 250.93	310.70	- -	03/2024	23.82
87	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	04/2012	255.64 - 255.64	272.20	- -	09/2021	6.48
88	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]	04/1987	406.99 - 406.99	545.70	03/2006 -	03/2025	34.08
89	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]	04/2007	450.00 - 450.00	1,261.34	- -	03/2025	180.30
90	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 - 172.03	260.10	- -	03/2025	51.19
91	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 - 915.98	2,137.81	03/2022 -	03/2025	133.39
92	BANDEL-BOINCHI 3RD LINE - [N22000221]	04/2011	288.35 - 288.35	402.48	- -	03/2020	39.58
93	PIRPAINTI-BHAGALPUR - [N22000222]	04/2011	261.38 - 261.38	492.84	- -	05/2019	88.55
94	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]	04/2001	923.52 - 923.52	995.10	03/2016 -	03/2025	7.75
95	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL [N22000225]	04/2005	595.51 - 595.51	769.40	03/2017 -	03/2025	29.20
<u>Indian Railway Construction Company Limited</u>							
96	GEVRA ROAD PENDRA ROAD - [N22000488]	02/2014	2,288.00 - 2,288.00	4,970.11	03/2022 -	12/2022	117.23
<u>Metropolitan Rapid Transport Projects</u>							
97	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 - 1,049.69	3,404.92	12/2006 -	-	224.37
98	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 - 1,781.98	2,980.41	03/2004 -	03/2021	501.57
99	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 - 495.74	734.01	06/2013 -	-	48.06
100	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	03/2013	4,874.58 - 4,874.58	8,574.97	03/2016 -	06/2021	75.91
<u>North Central Railway</u>							

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(January 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
101	ETAWAH-MAINPURI (NL),NCR - [220100318	04/1997	120.00 - 120.00	346.00	12/2008 -	-	188.33
102	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	04/2011	2,912.96 - 2,912.96	3,845.60	03/2022 -	12/2024	32.02
103	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372	04/2015	668.70 668.00 668.00	680.00	03/2020 -	03/2020	1.80
	<u>North East Frontier Railway</u>						
104	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135	04/1983	297.32 - 297.32	614.00	03/2019 -	03/2020	106.51
105	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	2,393.47 - 4,968.00	5,021.45	03/2014 -	03/2022	109.80
106	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	1,180.19 - 3,300.00	4,541.00	12/2008 -	03/2021	284.77
107	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124	04/2006	2,326.52 - 2,326.52	5,806.81	03/2015 -	10/2021	149.59
108	KISHANGANJ JALALGARH, NL, NEFR - [N22000101	04/2008	333.76 - 333.76	360.00	- -	03/2022	7.86
109	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 - 1,339.48	4,084.69	12/2015 -	-	204.95
110	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183	04/2013	1,798.00 - 1,798.00	2,496.67	03/2019 -	-	38.86
111	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193	04/2010	221.42 - 221.42	380.00	- -	03/2022	71.62
112	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205	04/2010	906.46 - 906.46	6,000.60	03/2021 -	03/2021	561.98
113	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206	04/2010	242.22 - 242.22	471.00	03/2020 -	03/2020	94.45
114	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207	04/2010	241.52 - 241.52	373.87	- -	06/2021	54.80
115	MURKONGSELEK-PASIGHAT NL - [N22000208	04/2011	414.84 - 414.84	661.00	03/2020 -	03/2020	59.34
116	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209	04/1999	819.23 - 819.23	1,871.00	- -	-	128.39

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(January 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
117	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 - 870.96	2,136.01	03/2021 -	03/2021	145.25
118	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) [N22000390]	04/2016	602.27 - 602.27	612.00	12/2021 -	03/2020	1.62
119	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]	02/1999	380.60 - 380.60	1,871.00	04/2010 -	-	391.59
<u>North Eastern Railway</u>							
120	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	142.45 - 142.45	228.40	- -	-	60.34
121	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 - 182.92	197.73	- -	-	8.10
122	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 - 307.00	1,409.09	- -	-	358.99
123	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 - 243.78	895.00	12/2021 -	12/2021	267.13
124	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 - 295.00	477.31	01/2019 -	01/2020	61.80
125	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 - 643.00	644.00	- -	-	.16
126	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 - 213.00	213.35	04/2016 -	06/2020	.16
127	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]	04/2017	1,343.00 - 1,343.00	1,476.15	01/2018 -	-	9.91
128	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]	04/2016	602.50 - 602.50	714.34	- -	-	18.56
<u>North Western Railway</u>							
129	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 - 780.98	886.41	02/2019 -	06/2021	116.16
130	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 - 600.00	685.99	03/2020 -	04/2022	14.33
131	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL [N22000330]	05/2015	873.71 - 873.71	1,980.21	- -	-	126.64

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(January 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
132	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 - 246.08	348.55	12/2019 -	02/2021	41.64
133	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 - 2,082.75	4,262.36	- -	-	104.65
134	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 - 236.93	350.45	10/2018 -	12/2019	47.91
135	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]	04/2013	822.00 - 822.00	1,099.54	- -	-	33.76
136	PUSHKAR-MERTA - [N22000151]	04/2013	323.00 - 323.00	432.22	- -	-	33.81
137	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 - 213.39	303.56	11/2019 -	12/2020	42.26
138	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 - 281.03	410.00	02/2019 -	02/2020	69.36
	<u>Northern Railway</u>						
139	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 - 156.65	197.17	- -	03/2024	25.87
140	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 - 695.00	750.00	12/2011 -	03/2021	161.32
141	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]	04/2007	336.91 - 336.91	791.39	- -	03/2022	134.90
142	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 - 219.83	346.63	- -	06/2020	57.68
143	UNCHAHAAR-AMETHI - [N22000294]	04/2012	1,229.00 - 1,229.00	1,230.00	- -	03/2023	.08
144	QADIAN-BEAS - [N22000295]	04/2011	205.22 - 205.22	841.90	- -	03/2024	310.24
145	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 - 2,010.00	2,200.00	07/2012 -	03/2024	388.89
146	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 - 328.14	1,540.00	03/2023 -	03/2023	369.31
147	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 - 625.00	859.00	03/2016 -	03/2021	37.44

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(January 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>Rail Vikas Nigam Ltd.</u>						
148	HARIDASPUR-PARADEEP(NL) - [N220100285]	04/1996	1,185.64 - 1,185.64	1,844.47	12/2017 -	03/2020	55.57
149	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [N220100327]	04/2000	133.41 207.00 207.00	396.00	03/2009 03/2009	06/2020	91.30
150	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	04/2010	2,913.51 - 2,913.51	4,639.00	03/2016 -	03/2025	59.22
151	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	2,966.99 - 2,966.99	7,000.00	12/2026 -	12/2025	135.93
152	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 - 2,127.00	2,900.00	03/2023 -	03/2024	36.34
153	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 - 3,951.98	4,724.30	03/2016 -	03/2025	19.54
154	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 - 2,298.42	2,733.86	03/2014 -	12/2025	18.95
155	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]	03/2012	1,503.71 - 1,503.71	2,200.00	03/2020 -	03/2022	46.30
156	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	975.62 - 975.62	1,082.32	12/2021 -	12/2021	10.94
157	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 - 632.68	816.55	03/2016 -	12/2020	29.06
158	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 - 3,246.26	3,548.67	12/2023 -	12/2023	9.32
159	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 - 927.01	1,200.00	03/2019 -	03/2020	29.45
160	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 - 713.48	2,300.00	03/2020 -	03/2021	222.36
161	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 - 2,335.67	2,335.68	12/2024 -	12/2024	.00
162	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 - 948.04	1,500.00	03/2020 -	03/2021	58.22
163	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 - 942.95	1,120.00	03/2019 -	06/2022	18.78

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(January 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>Railway Electrification</u>						
164	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 - 171.10	275.08	03/2012 -	-	60.77
	<u>South Central Railway</u>						
165	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	164.36 - 164.36	1,050.00	02/2009 -	-	538.84
166	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	1,723.00 1.00 1,780.29	3,472.59	03/2000 -	03/2021	3,47,159.00
167	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	458.25 - 458.25	458.26	- -	-	.00
168	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	04/2017	119.73 185.00 176.17	449.39	03/2022 -	12/2022	142.91
	<u>South Eastern Railway</u>						
169	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30 154.30	1,026.00	03/2007 03/2007	-	564.94
170	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 - 148.77	377.00	12/2016 -	03/2020	153.41
171	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 - 267.37	620.00	- -	03/2025	131.89
172	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	651.00 - 651.00	1,009.00	03/2015 -	03/2025	54.99
173	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 - 149.90	230.00	03/2015 -	-	53.44
174	BONDAMUNDA RANCHI DOUBLING - [N22000396]	03/2016	1,724.20 - 1,724.20	1,993.24	03/2021 -	12/2021	15.60
175	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 - 1,966.70	2,373.00	03/2003 -	03/2030	130.97
	<u>South Western Railway</u>						
176	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 - 146.75	167.50	- -	12/2023	14.14
177	YELAHANKA-PENUKONDA - [N22000328]	05/2015	860.43 - 860.43	958.00	03/2020 -	03/2020	11.34

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(January 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
178	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78 - 644.78	890.00	03/2017 -	03/2020	38.03
	<u>Southern Railway</u>						
179	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI [N22000079]	09/2007	724.69 - 724.69	2,072.50	02/2019 -	02/2020	185.98
180	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	227.40 - 227.40	900.00	- -	-	295.78
181	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	582.83 - 582.83	2,300.00	- -	-	294.63
182	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	303.98 - 303.98	980.00	03/2020 -	03/2021	222.39
183	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	1,566.00 - 1,566.00	2,815.62	- -	-	79.80
184	ATTIPPATTU PUTTUR - [N22000184]	04/2008	151.84 - 151.84	1,105.00	02/2019 -	-	627.74
185	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 - 523.52	2,300.00	- -	-	339.33
186	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 - 839.00	1,500.00	- -	-	78.78
187	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 - 198.68	556.64	- -	-	180.17
188	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 - 270.14	457.08	- -	-	69.20
189	ERODE-PALANI - [N22000199]	04/2008	288.57 - 288.57	1,140.00	- -	-	295.05
190	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 - 164.41	450.00	- -	03/2020	173.71
191	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	931.98 - 931.98	951.24	- -	03/2020	2.07
192	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70 - 120.70	1,800.00	03/2019 -	12/2019	1,391.30
193	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM [N22000373]	10/2013	187.26 - 187.26	231.67	04/2014 -	03/2020	23.72

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(January 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
194	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	02/1996	268.87 - 268.87	950.00	03/2005 -	-	253.33
195	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00 - 760.00	1,182.31	03/2020 -	06/2021	55.57
	<u>West Central Railway</u>						
196	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60 - 424.60	2,909.99	03/2021 -	03/2023	585.35
197	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 - 247.66	8,248.50	05/2008 -	03/2023	3,230.57
198	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13 - 582.13	1,247.64	03/2022 -	09/2022	114.32
	<u>Western Railway</u>						
199	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) [N22000125]	04/2006	117.36 196.95 196.95	202.35	03/2011 -	-	2.74
200	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	04/2008	829.74 - 1,215.34	1,310.23	03/2020 -	03/2021	57.91
201	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 - 858.56	858.96	03/2019 -	03/2022	167.87
	Total		1,18,770.70 5,039.25 1,31,610.71	2,34,600.00			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
202	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]	12/2011	156.26 227.00 227.00	247.95	- -	-	9.23
203	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]	11/2010	624.41 - 624.41	992.67	03/2011 -	12/2020	58.98
204	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]	08/2010	193.69 - 193.69	327.92	10/2010 -	06/2021	69.30
205	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM [N24000314]	01/2013	182.28 - 182.28	269.14	02/2013 -	12/2019	47.65
206	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]	03/2015	258.97 - 258.97	268.92	08/2015 -	-	3.84

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(January 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
207	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259	03/2015	280.16 - 280.16	290.59	- -	-	3.72
208	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00 348.00	348.43	09/2017 -	-	.12
209	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371	10/2013	445.89 -	653.29	03/2017 -	-	46.51
210	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388	11/2013	497.05 -	881.05	05/2017 -	05/2020	77.26
211	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396	11/2010	470.20 -	630.36	02/2011 -	-	34.06
212	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398	01/1991	282.41 -	322.01	08/2016 -	-	14.02
213	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402	01/1991	358.22 -	377.64	10/2016 -	-	5.42
214	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407	10/2015	333.21 -	353.89	11/2015 -	-	6.21
215	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411	11/2014	218.31 -	307.47	02/2018 -	-	40.84
216	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415	08/2010	195.04 -	377.99	10/2010 -	-	93.80
217	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531	01/1991	319.68 -	369.77	- -	-	15.67
218	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646	06/2016	157.30 157.00 157.00	157.30	06/2018 -	-	.19
219	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782	03/2018	460.73 -	461.00	- -	-	.06
220	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820	11/2017	237.80 -	238.00	11/2019 -	-	.08
221	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH.0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928	10/2015	333.21 -	355.89	12/2015 -	01/2020	6.81
222	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938	03/2018	297.12 294.00 294.00	294.12	07/2018 -	01/2020	.04

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(January 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
223	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]	03/2018	504.19 504.00 504.00	504.19	11/2018 -	05/2020	.04
224	REHABILITATION AND UPGRADATION OF KARNATAKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]	03/2016	995.09 995.00 995.00	995.09	05/2016 -	07/2020	.01
225	KHAMGAON TO SHEGAON - [N24001009]	02/2017	203.21 203.00 203.00	203.21	05/2019 -	12/2019	.10
226	SHEGAON TO DEORI PHATA - [N24001010]	02/2017	373.10 373.00 373.00	373.10	05/2019 -	12/2019	.03
227	MEHKAR TO CHIKALI - [N24001011]	02/2017	322.48 322.00 322.00	322.48	05/2019 -	-	.15
228	CHIKALI TO KHAMGAON - [N24001012]	02/2017	548.03 548.00 548.00	548.03	06/2019 -	10/2019	.01
229	DIGRAS DARWAH KARANJA - [N24001013]	01/2017	391.06 391.00 391.00	391.06	06/2019 -	06/2020	.02
230	MORSHI TO ACHALPUR - [N24001015]	01/2017	341.16 341.00 341.00	341.16	06/2019 -	-	.05
231	KARAD TO VITA - [N24001049]	01/2018	344.85 245.00 245.00	344.85	12/2019 -	12/2019	40.76
232	SANGOLA TO JATH - [N24001052]	01/2018	257.38 257.00 257.00	257.38	12/2019 -	12/2019	.15
233	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]	02/2017	422.02 422.00 422.00	422.02	07/2019 -	-	.00
234	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]	02/2017	407.19 407.00 407.00	407.19	06/2019 -	06/2020	.05
235	PALPHATA TO PHULAMBAR - [N24001060]	03/2018	227.19 227.00 227.00	227.19	12/2019 -	12/2019	.08
236	CHIKALI TO DHAD - [N24001061]	03/2018	189.46 189.00 189.00	189.46	12/2019 -	12/2019	.24
237	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]	03/2018	336.21 336.00 336.00	336.21	12/2019 -	12/2019	.06
238	WADIGODRI TO DHANGRIIMPRI - [N24001063]	03/2018	194.23 194.00 194.00	194.23	02/2020 -	02/2020	.12

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(January 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
239	DHANGIPIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]	03/2018	217.14 217.00 217.00	217.14	02/2020 -	02/2020	.06
240	PARBHANI TO GANGKHED - [N24001065]	03/2018	238.19 238.00 238.00	238.19	12/2019 -	12/2019	.08
241	LATUR TO PANGAON - [N24001066]	03/2018	336.47 336.00 336.00	336.47	12/2019 -	12/2019	.14
242	OMREGA TO AUSA - [N24001067]	03/2018	272.04 272.00 272.00	272.04	12/2019 -	12/2019	.01
243	KOTHARI TO DHANORA - [N24001073]	09/2018	301.38 301.00 301.00	301.38	08/2020 -	08/2020	.13
244	OSMANNAGAR TO KUNDRAL - [N24001075]	09/2017	344.25 344.00 344.00	344.25	08/2020 -	08/2020	.07
245	KUNDRAL TO WAZAR - [N24001077]	01/2018	225.25 225.00 225.00	225.25	12/2019 -	12/2019	.11
246	ARDHAPUR TO HIMAYATNAGAR - [N24001079]	12/2017	426.06 426.00 426.00	426.06	06/2020 -	06/2020	.01
247	JALGAON TO NANDURA - [N24001088]	03/2018	177.84 177.00 177.00	177.84	12/2019 -	12/2019	.47
248	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]	03/2016	536.65 356.00 356.00	536.65	12/2019 -	12/2019	50.74
249	NAIGAONBANDI TO MANGRULPIR - [N24001094]	12/2017	244.04 244.00 244.00	244.04	03/2019 -	12/2019	.02
250	TALEGAON TO GONAPUR - [N24001096]	01/2018	264.41 264.00 264.00	264.41	03/2019 -	12/2019	.16
251	SELDOH TO PANVAR - [N24001097]	07/2018	404.33 404.00 404.00	404.33	05/2020 -	05/2020	.08
252	PANCHARAL TO MANDANGHAR - [N24001107]	07/2018	381.08 302.00 302.00	381.08	05/2020 -	05/2020	26.19
253	VADPALE TO BHOGAN KHURD - [N24001115]	01/2017	1,598.47 1,560.00 1,560.00	1,598.47	11/2019 -	03/2020	2.47
254	BHOKAR TO SARSAM - [N24001128]	02/2017	295.09 - 295.09	295.99	07/2019 -	-	.31

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(January 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
255	BHOGAN KHURD TO KASHEDI - [N24001132]	09/2017	743.21 743.00 743.00	743.21	06/2021 -	06/2021	.03
256	PARSHURAM GHAT TO ARAWALI - [N24001133]	04/2016	983.14 983.00 983.00	983.14	12/2019 -	-	.01
257	KANTE TO WAKED - [N24001134]	03/2016	1,230.02 1,230.00 1,230.00	1,230.02	11/2019 -	-	.00
258	KALMATH TO ZARAP - [N24001137]	09/2016	1,338.13 1,338.00 1,338.00	1,338.13	03/2020 -	03/2020	.01
259	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]	11/2016	215.16 215.00 215.00	215.16	09/2019 -	10/2019	.07
260	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]	03/2016	240.30 240.00 240.00	240.30	01/2020 -	03/2020	.13
261	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]	10/2013	445.89 653.00 653.00	653.29	03/2017 -	10/2019	.04
262	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]	08/2010	186.96 - 186.96	305.61	09/2014 -	06/2020	63.46
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
263	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]	04/2017	388.00 - 388.00	447.37	10/2017 -	-	15.30
264	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]	03/2018	237.72 - 136.73	237.72	09/2018 -	-	.00
265	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]	03/2018	251.97 - 160.10	251.97	09/2018 -	-	.00
	<u>National Highways Authority Of India</u>						
266	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]	12/2003	160.00 - 160.00	167.98	05/2008 -	06/2019	4.99
267	INDORE-DEWAS(NH-3) - [N24000159]	11/2010	325.00 - 325.00	475.00	05/2013 -	-	46.15
268	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61 - 217.61	360.84	04/2010 -	07/2019	65.82
269	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 - 208.00	230.00	04/2008 -	03/2020	10.58

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(January 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
270	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	04/2014	1,266.60 - 1,266.60	1,544.00	09/2016 -	-	21.90
271	NASHRI- CHANANI - [N24000162]	05/2011	2,159.00 - 2,159.00	2,519.00	06/2015 -	-	16.67
272	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]	05/2011	511.54 - 585.00	591.00	11/2013 -	03/2020	15.53
273	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 - 1,928.22	2,945.00	04/2015 -	06/2020	52.73
274	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]	10/2015	531.13 - 531.13	727.00	05/2018 -	09/2020	36.88
275	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]	10/2015	593.26 - 41.54	636.24	05/2018 -	06/2020	7.24
276	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]	06/2015	845.24 - 845.24	941.00	- -	01/2020	11.33
277	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]	03/2015	795.76 - 659.57	677.72	- -	03/2020	-14.83
278	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]	03/2015	794.30 - 637.86	691.38	- -	12/2019	-12.96
279	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]	08/2015	814.04 - 814.04	825.17	- -	-	1.37
280	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	05/2013	1,055.00 - 1,055.00	1,601.77	11/2015 -	-	51.83
281	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]	01/1991	642.41 - 642.41	681.67	- -	10/2020	6.11
282	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]	07/2015	1,871.34 - 67.34	1,871.34	01/2018 -	03/2020	.00
283	MEERUT-BULANDSHAHAH - [N24000539]	01/2016	683.24 - 868.77	987.94	- -	02/2020	44.60
284	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]	03/2016	197.69 - 151.11	197.69	07/2018 -	-	.00
285	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]	03/2016	1,587.49 - 1,587.49	2,982.00	04/2019 -	-	87.84

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(January 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
286	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]	05/2016	425.60 - 241.41	425.60	- -	-	.00
287	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]	05/2016	364.56 - 364.56	392.00	- -	08/2020	7.53
288	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]	08/2016	1,388.34 - 2,541.32	2,587.50	09/2019 -	03/2020	86.37
289	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]	09/2016	950.69 - 1,008.00	1,108.00	08/2019 -	12/2020	16.55
290	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]	09/2016	1,100.19 - 1,100.19	1,145.31	- -	05/2020	4.10
291	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]	11/2012	605.84 - 605.84	722.46	07/2018 -	02/2020	19.25
292	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	03/2017	1,184.71 - 1,184.71	1,310.00	03/2020 -	08/2020	10.58
293	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	03/2017	744.64 - 744.64	982.00	03/2020 -	03/2020	31.88
294	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	03/2017	1,030.44 - 1,030.44	1,065.51	03/2020 -	05/2020	3.40
295	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	03/2017	988.34 - 988.00	1,043.28	03/2020 -	08/2020	5.56
296	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]	03/2017	1,059.73 - 1,059.73	1,071.00	03/2017 -	11/2020	1.06
297	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]	03/2017	1,098.06 - 1,098.06	1,160.64	03/2020 -	08/2020	5.70
298	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	03/2017	754.54 - 754.54	756.27	03/2020 -	08/2021	.23
299	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	03/2017	672.89 - 672.89	736.01	03/2020 -	03/2020	9.38
300	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]	03/2017	1,041.62 - 1,041.62	1,187.10	03/2020 -	05/2020	13.97
301	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]	03/2017	165.50 - 165.50	172.16	03/2020 -	03/2020	4.02

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(January 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
302	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 - 1,288.07	1,420.00	03/2020 -	03/2021	10.24
303	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 - 2,064.99	2,447.00	03/2020 -	06/2020	18.50
304	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 - 831.58	1,177.00	03/2020 -	07/2020	41.54
305	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 - 993.16	1,434.00	03/2020 -	06/2020	44.39
306	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691	04/2017	894.00 - 894.00	929.32	04/2020 -	04/2020	3.95
307	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704	09/2017	1,124.11 - 1,124.11	1,232.76	09/2017 -	05/2021	9.67
308	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729	01/2018	607.00 - 512.99	607.00	- -	08/2021	.00
309	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730	01/2018	621.00 - 565.02	621.00	- -	04/2021	.00
310	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784	02/2018	1,424.77 - 1,424.77	1,853.42	- -	-	30.09
311	SIX-LANING OF BANGALORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787	02/2018	1,995.34 - 2,190.00	2,400.00	- -	11/2021	20.28
312	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789	02/2018	2,177.80 - 2,283.50	2,450.00	- -	-	12.50
313	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814	03/2018	1,029.96 - 1,029.96	1,261.05	- -	03/2021	22.44
314	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829	03/2018	1,016.92 - 1,016.92	1,071.00	- -	04/2021	5.32
315	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830	03/2018	2,065.96 - 2,065.96	2,169.00	- -	-	4.99
316	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831	03/2018	1,294.47 - 1,294.47	1,296.00	- -	-	.12
317	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842	03/2018	199.90 - 149.90	199.90	- -	-	.00

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(January 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
318	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841	03/2018	795.50 - 795.50	799.30	- -	07/2021	.48
319	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843	03/2018	196.05 - 149.90	196.05	- -	01/2020	.00
320	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853	03/2018	642.13 - 642.13	807.00	- -	12/2020	25.68
	Total		77,163.00 18,048.00 75,575.45	89,381.14			
	<u>TELECOMMUNICATIONS</u>						
	<u>Department Of Telecommunication</u>						
321	NETWORK FOR SPECTRUM - [N26000101	03/2012	13,334.00 - 13,334.00	24,664.00	07/2015 -	05/2020	84.97
	Total		13,334.00 .00 13,334.00	24,664.00			
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
322	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 - 1,219.21	2,000.00	10/2019 -	03/2021	64.04
323	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100	02/2016	496.18 496.00 496.00	498.99	06/2017 -	03/2021	.60
	<u>Chennai Metro Rail Ltd</u>						
324	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084	02/2009	14,600.00 - 14,600.00	19,058.00	12/2015 -	-	30.53
	<u>Hindustan Steelwork Construction Limited</u>						
325	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101	05/2005	768.88 1,070.97 1,070.97	1,113.34	02/2014 -	-	3.96
326	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098	03/2007	149.73 173.00 173.00	175.94	12/2015 -	-	1.70
	<u>Kochi Metro Rail Corporation Ltd</u>						
327	KOCHI METRO RAIL PROJECT - [N28000081	07/2012	5,181.79 - 5,687.79	6,218.14	07/2017 -	03/2020	20.00

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(January 2020)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	Total		22,415.79 1,739.97 23,246.97	29,064.41			
	Grand Total		4,19,968.92 29,065.22 4,36,882.60	6,27,651.37			

List of Delayed Projects w.r.t. Latest Schedule

Annexure-XIV

Costing Rs. 150 Crore and above (January 2020)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
	<u>Bhavini Limited</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 5,677.00	6,840.00	5,862.38	09/2010 09/2016	10/2021	133	61
	<u>Nuclear Power Corporation Of India Limited</u>								
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	16,580.00	14,629.00	12/2015 -	09/2021	69	-
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	17,079.00	11,737.00	12/2016 -	03/2023	75	-
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL,TAMIL NADU	03/2013	39,849.00 -	39,849.00	17,987.00	11/2020 -	11/2023	36	-
	Total		67,120.00 -	80,348.00	50,215.38				
	<u>CIVIL AVIATION</u>								
	<u>Airport Authority Of India Limited</u>								
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,A & N ISLANDS	10/2013	314.61 -	441.33	85.79	09/2018 -	06/2020	21	-
6	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076]AAI,DELHI	11/2016	233.38 -	233.38	84.73	04/2020 -	12/2020	8	-
7	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA - [N04000080]AAI,WEST BENGAL	01/2016	219.91 -	219.91	65.45	03/2020 -	12/2020	9	-
8	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI - [N04000074]AAI,TAMIL NADU	06/2018	2,467.00 -	2,467.00	213.17	02/2022 -	08/2022	6	-
	Total		3,234.90 -	3,361.62	449.14				
	<u>COAL</u>								
	<u>Bharat Coking Coal Limited</u>								
9	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	269.82	181.30	04/2014 -	03/2020	71	-
10	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	289.45	263.37	05/2014 03/2020	05/2020	72	2
	<u>Central Coal Fields Limited</u>								
11	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	107.16	03/2011 -	03/2021	120	-
12	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	181.17	03/2012 -	03/2021	108	-
13	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	399.09	03/2016 -	03/2021	60	-
14	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	90.75	03/2014 -	03/2021	84	-

Costing Rs. 150 Crore and above

(January 2020)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
15	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	706.40 -	706.40	501.09	07/2012 -	03/2022	116	-
	<u>Eastern Coal Fields Limited</u>								
16	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05 -	1,055.05	562.60	03/2018 -	10/2020	31	-
17	RANIGANJ MASTER PLAN - [N06000163]ECL,WEST BENGAL	08/2009	2,661.73 -	5,146.48	364.72	08/2019 -	08/2024	60	-
	<u>Mahanadi Coal Fields Limited</u>								
18	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	270.32	03/2010 -	03/2020	120	-
19	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.10 -	490.10	524.33	03/2017 -	03/2021	48	-
20	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	306.94	03/2012 -	03/2021	108	-
21	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA	05/2014	337.66 -	337.66	215.55	03/2019 -	03/2021	24	-
22	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA	06/2014	289.03 -	289.03	-	03/2018 -	03/2021	36	-
23	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	568.14	03/2013 -	03/2022	108	-
24	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	377.07	03/2010 -	03/2022	144	-
25	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	479.53	445.05	03/2013 -	03/2022	108	-
26	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA	05/2014	479.15 -	479.15	214.07	03/2019 -	03/2024	60	-
	<u>Neyveli Lignite Corporation</u>								
27	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 7,080.41	7,080.41	6,954.15	12/2015 -	03/2020	51	-
	<u>Singareni Colliers Company Limited</u>								
28	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78 -	209.78	137.06	03/2015 -	03/2020	60	-
29	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	171.06	06/2015 -	03/2020	57	-
30	KALYANIKHANI OPENCASE PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	384.32	115.04	07/2016 -	03/2020	44	-
31	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 -	415.37	189.54	03/2016 -	03/2020	48	-
32	KAKATIYAKHANI OPENCASE-2 PROJECT - [N06000129]SCCL,TELANGANA	05/2015	397.09 -	442.42	99.56	03/2019 -	03/2020	12	-
33	KOYAGUDEM OPENCASE PROJECT - [N06000146]SCCL,TELANGANA	10/2015	426.79 -	426.79	.72	03/2018 -	03/2020	24	-
34	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL,TELANGANA	11/2016	272.73 -	272.73	153.75	- 04/2017	03/2020	-	35
35	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	164.04	120.31	03/2015 -	03/2021	72	-
36	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	349.28	12.27	03/2015 -	03/2021	72	-
37	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	473.22	18.60	03/2015 -	03/2021	72	-

Costing Rs. 150 Crore and above

(January 2020)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
38	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]SCCL,TELANGANA	03/2017	413.84 -	413.84	123.18	03/2019 -	03/2022	36	-
39	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	489.62	416.88	03/2012 -	03/2023	132	-
40	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	448.86	326.69	03/2012 -	03/2024	144	-
	<u>South-Eastern Coal Fields Limited</u>								
41	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	2.92	03/2014 -	03/2020	72	-
42	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56 -	258.56	182.04	03/2016 -	03/2020	48	-
43	AMERA OC RCE - [N06000123]SECL,CHHATISGARH	02/2015	335.97 -	335.97	51.21	03/2018 -	03/2020	24	-
44	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	197.36	03/2014 -	03/2021	84	-
45	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL,CHHATISGARH	06/2010	11,816.40 -	11,816.40	2,920.18	03/2023 03/2016	03/2023	0	84
	<u>Western Coal Fields Limited</u>								
46	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA	08/2015	288.90 -	333.43	38.82	03/2023 -	03/2024	12	-
47	KAMPTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA	11/2015	277.65 -	313.34	118.18	03/2021 -	03/2024	36	-
	Total		33,137.17 -	37,277.59	17,922.24				
	<u>FERTILISERS</u>								
	<u>National Fertiliser Limited</u>								
48	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]NFL,PUNJAB	01/2018	218.83 -	218.83	142.01	11/2019 -	05/2020	6	-
49	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]NFL,PUNJAB	01/2018	239.81 -	239.81	156.70	11/2019 -	05/2020	6	-
	Total		458.64 -	458.64	298.71				
	<u>STEEL</u>								
	<u>Steel Authority Of India Limited (Sail)</u>								
50	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND	05/2015	1,154.18 -	1,154.18	998.53	12/2017 01/2020	03/2020	27	2
51	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND	11/2016	262.87 -	262.87	131.30	06/2019 06/2020	11/2020	17	5
	Total		1,417.05 -	1,417.05	1,129.83				
	<u>PETROLEUM</u>								
	<u>Bharat Petroleum Corporation Limited</u>								
52	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA	11/2014	4,588.29 5,245.96	5,245.96	4,137.20	08/2018 11/2019	02/2020	18	3

Costing Rs. 150 Crore and above

(January 2020)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
53	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 -	678.00	8.10	02/2017 -	10/2021	56	-
	<u>Chennai Petroleum Corporation Limited</u>								
54	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU	09/2017	1,858.00 -	1,858.00	1,229.51	12/2019 -	04/2020	4	-
55	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU	08/2017	421.00 -	421.00	177.80	08/2020 -	02/2021	6	-
	<u>Gas Authority Of India Limited</u>								
56	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT	04/2016	327.78 -	200.00	155.59	04/2018 -	02/2020	22	-
	<u>Hindustan Petroleum Corporation Limited</u>								
57	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA	06/2017	249.26 -	249.26	62.55	06/2020 -	09/2021	15	-
58	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]HPCL,JHARKHAND	06/2017	161.50 -	161.50	17.78	06/2020 -	09/2021	15	-
	<u>Indian Oil Corporation Limited</u>								
59	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]IOCL,UTTAR PRADESH	01/2018	666.64 -	666.64	493.90	09/2019 -	01/2020	4	-
60	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]IOCL,ASSAM	02/2016	2,582.00 -	2,582.00	1,704.47	11/2019 -	02/2020	3	-
61	BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]IOCL,GUJARAT	03/2018	3,380.00 -	3,380.00	2,346.62	09/2019 -	02/2020	5	-
62	BS-VI PROJECT AT BONGAIGAON REFINERY - [N16000320]IOCL,ASSAM	05/2018	1,222.00 -	1,222.00	739.04	09/2019 -	02/2020	5	-
63	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY - [N16000322]IOCL,WEST BENGAL	05/2018	2,934.40 -	2,934.40	1,928.10	09/2019 -	02/2020	5	-
64	BS-VI PROJECT AT PANIPAT REFINERY - [N16000325]IOCL,HARYANA	12/2017	3,529.00 -	3,529.00	2,088.18	07/2019 -	02/2020	7	-
65	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]IOCL,ASSAM	08/2018	557.00 -	557.00	313.62	02/2020 -	04/2020	2	-
66	FUEL QUALITY UPGRADATION (NSU,NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY - [N16000348]IOCL,BIHAR	06/2017	951.64 -	951.64	552.00	10/2019 -	05/2020	7	-
67	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]IOCL,ODISHA	05/2016	429.00 -	429.00	329.59	01/2019 -	06/2020	17	-
68	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	351.04	07/2018 -	10/2020	27	-
69	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND	02/2017	160.10 -	160.10	54.94	02/2020 -	10/2020	8	-
70	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]IOCL,MADHYA PRADESH	08/2017	236.00 -	236.00	49.62	06/2020 -	10/2020	4	-
71	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT	10/2017	906.00 -	906.00	123.94	02/2020 -	10/2020	8	-

Costing Rs. 150 Crore and above

(January 2020)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
72	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM	06/2016	423.00 -	423.00	363.66	08/2019 -	12/2020	16	-
73	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]IOCL,HARYANA	04/2018	206.63 -	206.63	29.25	02/2020 -	12/2020	10	-
74	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]IOCL,HARYANA	10/2018	598.00 -	598.00	27.18	02/2020 -	01/2021	11	-
75	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU	05/2016	4,497.00 6,025.00	6,025.00	1,588.02	12/2018 -	02/2021	26	-
76	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL,WEST BENGAL	04/2017	163.02 -	163.02	59.14	04/2020 -	03/2021	11	-
77	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00 -	212.00	57.97	01/2021 -	04/2021	3	-
78	LPG BP PROJECT KHRDHA - [N16000283]IOCL,ODISHA	12/2016	161.59 -	161.59	40.21	12/2019 -	07/2021	19	-
79	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH	08/2018	466.00 -	466.00	124.36	04/2021 -	07/2021	3	-
80	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	466.43	68.41	10/2020 -	08/2021	10	-
81	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]IOCL,HARYANA	01/2019	909.00 -	909.00	23.71	01/2021 -	08/2021	7	-
82	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 -	348.00	101.41	01/2021 -	10/2021	9	-
83	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	318.80	63.90	08/2021 -	11/2021	3	-
84	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	355.00	29.38	04/2022 -	02/2023	10	-
85	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA	12/2018	611.00 -	611.00	13.32	04/2022 -	03/2023	11	-
<u>Mangalore Refinery And Petrochemicals Limited</u>									
86	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA	09/2016	1,810.00 1,810.00	1,810.00	1,022.88	12/2019 07/2020	03/2021	15	8
<u>Oil & Natural Gas Corporation Limited</u>									
87	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]ONGC,MAHARASHTRA	02/2019	3,660.71 3,740.05	3,740.05	373.79	04/2021 -	05/2021	1	-
88	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH	03/2016	34,012.00 -	34,012.00	4,995.31	06/2020 -	08/2021	14	-

Costing Rs. 150 Crore and above

(January 2020)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
89	HEERA REDEVELOPMENT - PHASE III - [N16000360]ONGC,MAHARASHTRA	05/2019	2,494.68 -	2,494.68	270.26	12/2021 -	03/2022	3	-
	<u>Oil India Limited</u>								
90	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM	01/2018	543.91 -	682.90	71.46	02/2020 -	06/2020	4	-
	Total		78,784.38 -	81,060.60	26,187.21				
	<u>POWER</u>								
	<u>National Thermal Power Corporation</u>								
91	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC,MADHYA PRADESH	03/2015	9,870.51 -	11,148.86	9,430.15	01/2020 -	02/2020	1	-
92	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA	02/2014	12,532.44 -	13,740.53	10,182.96	12/2018 02/2020	08/2020	20	6
93	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC,ODISHA	05/2016	1,885.13 -	1,885.13	1,486.29	12/2018 -	08/2020	20	-
94	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC,WEST BENGAL	12/2016	529.68 -	529.68	294.18	11/2018 -	08/2020	21	-
95	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH	09/2014	9,188.98 -	10,016.10	7,036.74	07/2019 03/2020	09/2020	14	6
96	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 7,998.00	9,583.00	8,056.25	07/2012 -	09/2020	98	-
97	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA	01/2016	10,598.98 -	10,598.98	6,325.54	11/2020 02/2021	09/2021	10	7
98	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 5,867.38	5,867.38	4,346.71	03/2013 12/2020	12/2021	105	12
99	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 -	15,164.05	9,965.78	06/2019 09/2019	03/2022	33	30
100	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL	09/2014	1,381.84 -	1,592.34	526.08	09/2019 02/2022	11/2022	38	9
	<u>Power Grid Corporation Of India Limited</u>								
101	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 260.03	260.03	200.16	07/2017 06/2019	01/2020	30	7
102	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE	10/2016	608.24 -	608.24	425.04	04/2019 -	01/2020	9	-
103	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE	12/2015	3,654.00 -	3,654.00	3,508.04	04/2019 -	01/2020	9	-
104	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 639.46	639.46	590.30	06/2014 09/2019	02/2020	68	5
105	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 1,891.41	1,891.41	1,283.60	04/2016 08/2019	02/2020	46	6
106	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE	05/2016	3,519.59 -	3,519.59	2,562.41	05/2019 -	02/2020	9	-

Costing Rs. 150 Crore and above

(January 2020)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
107	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 5,071.94	5,071.94	4,595.36	10/2012 12/2019	03/2020	89	3
108	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 374.63	374.63	224.83	04/2016 12/2017	03/2020	47	27
109	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 5,151.37	5,151.37	3,269.93	03/2018 12/2019	03/2020	24	3
110	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE	01/2015	871.62 -	871.62	606.81	10/2017 09/2019	03/2020	29	6
111	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 197.40	197.40	85.34	03/2018 -	03/2020	24	-
112	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	1,394.52	457.17	05/2017 06/2019	03/2020	34	9
113	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE	05/2016	14,733.37 -	14,733.37	9,883.31	11/2019 -	03/2020	4	-
114	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE	10/2016	408.46 -	408.46	322.79	01/2019 09/2019	03/2020	14	6
115	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	235.53	138.98	06/2019 -	03/2020	9	-
116	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE	03/2017	379.95 -	379.95	113.54	12/2019 -	03/2020	3	-
117	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 -	186.17	111.47	07/2019 -	03/2020	8	-
118	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA	05/2017	445.89 -	445.89	332.46	02/2019 12/2019	05/2020	15	5
119	HVDC BIPOLE LINK BETWEEN WR AND SR - NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE	08/2017	1,931.39 -	1,931.39	1,164.36	02/2020 -	06/2020	4	-
120	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	9,072.36	1,402.48	12/2018 -	12/2020	24	-
121	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	6,880.36	1,886.30	12/2018 -	12/2020	24	-
	<u>Thdc India Limited</u>								
122	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	4,397.80	1,858.35	06/2013 -	12/2022	114	-

Costing Rs. 150 Crore and above

(January 2020)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	Total		1,22,014.49 -	1,42,431.54	92,673.71				
	<u>HEAVY INDUSTRY</u>								
	<u>Bharat Heavy Electricals Limited</u>								
123	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL,DELHI	08/2016	1,554.00 -	1,554.00	716.25	09/2019 -	03/2020	6	-
	Total		1,554.00 -	1,554.00	716.25				
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>HII Infra Tech Services Limited</u>								
124	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	715.06	385.77	04/2020 -	10/2020	6	-
125	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	557.48	327.76	06/2020 -	10/2020	4	-
126	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 -	747.80	137.27	05/2021 08/2021	10/2021	5	2
	<u>Hospital Services Consultancy Corporation Ltd</u>								
127	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	325.00	304.62	05/2017 -	01/2020	32	-
128	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	177.92	147.31	02/2018 -	03/2020	25	-
129	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	274.19	230.83	03/2019 -	03/2020	12	-
130	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	272.54	204.08	03/2019 -	03/2020	12	-
131	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	270.00	210.75	05/2017 -	06/2020	37	-
132	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	363.99	219.50	05/2018 -	07/2020	26	-
133	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL	08/2017	355.15 -	355.15	233.51	03/2019 -	07/2020	16	-
134	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	499.23	337.32	11/2013 -	09/2020	82	-
	Total		4,693.67 -	4,558.36	2,738.72				
	<u>RAILWAYS</u>								
	<u>Central Railways</u>								
135	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50 -	4,517.49	2,495.07	03/2021 -	03/2022	12	-
136	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89 -	1,377.48	318.59	03/2021 -	03/2022	12	-

Costing Rs. 150 Crore and above

(January 2020)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
137	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19 -	1,272.19	339.43	03/2022 -	03/2023	12	-
138	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02 -	540.02	265.90	03/2022 -	03/2024	24	-
139	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 -	1,035.16	138.46	03/2022 -	03/2024	24	-
140	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 -	637.95	76.12	03/2023 -	03/2024	12	-
	<u>Container Corporation Of India</u>								
141	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	174.00	164.41	03/2019 -	02/2020	11	-
142	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	493.17	443.19	03/2018 -	03/2020	24	-
143	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32 -	346.32	292.82	03/2019 -	03/2020	12	-
144	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	235.00	10.88	03/2019 -	12/2020	21	-
	<u>East Central Railways</u>								
145	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	324.73 898.53	1,050.00	1,041.96	03/2012 -	03/2020	96	-
146	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	477.88 751.55	751.55	674.58	03/2012 -	03/2020	96	-
147	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	678.54 678.54	678.54	556.86	03/2019 -	02/2021	23	-
148	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	681.43	03/2020 -	03/2021	12	-
149	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	528.57	128.55	03/2019 -	03/2021	24	-
150	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR	12/2015	1,200.20 1,200.20	1,200.20	586.83	03/2020 -	10/2021	19	-
151	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR	12/2015	1,491.47 -	1,491.47	448.67	03/2020 -	12/2021	21	-
152	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	548.00 819.01	819.01	525.18	03/2020 -	03/2022	24	-
153	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 1,215.54	1,215.54	156.95	03/2021 -	03/2022	12	-
154	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 1,185.73	1,185.73	60.65	03/2021 -	03/2022	12	-
	<u>East Coast Railway</u>								
155	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	238.03	205.65	03/2020 -	03/2021	12	-
156	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 701.61	810.02	139.27	11/2018 -	03/2022	40	-
157	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 1,172.92	1,172.92	560.36	12/2018 03/2022	03/2023	51	12
158	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 3,791.66	3,791.66	1,270.24	03/2009 -	06/2024	183	-
159	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 198.07	1,928.07	780.24	06/2021 -	06/2024	36	-

Costing Rs. 150 Crore and above

(January 2020)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
160	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 2,361.74	2,361.74	247.79	03/2022 -	03/2025	36	-
	<u>Eastern Railways</u>								
161	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	157.94	51.75	11/2018 -	03/2021	28	-
162	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	542.18 -	693.80	474.79	03/2020 -	03/2021	12	-
163	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	1,425.44	637.56	02/2013 -	03/2024	133	-
164	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	1,619.48	872.43	03/2019 12/2009	03/2025	72	183
165	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	1,106.62 -	1,091.59	877.32	12/2010 12/2017	03/2025	171	87
166	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	545.70	148.49	03/2006 -	03/2025	228	-
167	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	2,137.81	300.18	03/2022 -	03/2025	36	-
168	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	995.10	507.56	03/2016 -	03/2025	108	-
169	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.51 -	769.40	103.08	03/2017 -	03/2025	96	-
170	SONDALIA-CHAMPAPUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	266.32	169.37	03/2016 -	03/2025	108	-
171	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	296.43	275.76	03/2017 -	03/2025	96	-
172	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	494.59	32.00	03/2005 -	03/2025	240	-
173	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96 -	680.68	159.70	02/2012 -	03/2025	157	-
174	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	257.42	108.11	03/2014 -	03/2025	132	-
175	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	108	-
	<u>Indian Railway Construction Company Limited</u>								
176	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]JRCON,CHHATISGARH	04/2013	3,055.00 -	3,055.00	2,096.39	09/2018 -	03/2021	30	-
177	GEVRA ROAD PENDRA ROAD - [N22000488]JRCON,CHHATISGARH	02/2014	2,288.00 -	4,970.11	635.13	03/2022 -	12/2022	9	-

Costing Rs. 150 Crore and above

(January 2020)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
178	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRON,ODISHA	04/2016	5,200.00 -	1,700.43	48.00	03/2020 -	06/2023	39	-
	<u>Metropolitan Rapid Transport Projects</u>								
179	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 1,781.98	2,980.41	1,457.78	03/2004 -	03/2021	204	-
180	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 -	918.53	284.75	03/2014 -	03/2021	84	-
181	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	63	-
	<u>North Central Railway</u>								
182	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	2,912.96 -	3,845.60	148.26	03/2022 -	12/2024	33	-
	<u>North East Frontier Railway</u>								
183	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	297.32 -	614.00	275.07	03/2019 -	03/2020	12	-
184	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	385.20 1,532.00	1,532.00	652.15	03/2019 -	03/2020	12	-
185	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 2,145.00	2,145.00	935.62	03/2019 -	03/2020	12	-
186	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	314.00 728.00	728.00	731.27	03/2019 -	03/2020	12	-
187	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	1,180.19 3,300.00	4,541.00	3,346.08	12/2008 -	03/2021	147	-
188	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52 -	5,806.81	876.09	03/2015 -	10/2021	79	-
189	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	4,454.17 13,809.00	12,524.00	9,599.02	03/2011 -	03/2022	132	-
	<u>North Eastern Railway</u>								
190	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	477.31	370.93	01/2019 -	01/2020	12	-
191	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH	04/2017	622.50 427.00	426.74	240.48	04/2017 -	01/2020	33	-
192	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	213.35	9.63	04/2016 -	06/2020	50	-
193	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	1,028.95	26.06	12/2019 -	04/2021	16	-
194	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	276.90	-	04/2017 -	04/2022	60	-
195	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	150.00	-	04/2017 -	10/2022	66	-
	<u>North Western Railway</u>								
196	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 281.03	410.00	381.92	02/2019 -	02/2020	12	-

Costing Rs. 150 Crore and above

(January 2020)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
197	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	420.18 -	420.18	199.53	03/2020 -	12/2020	9	-
198	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	303.56	285.01	11/2019 -	12/2020	13	-
199	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	348.55	248.71	12/2019 -	02/2021	14	-
200	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 780.98	886.41	568.73	02/2019 -	06/2021	28	-
201	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	685.99	99.38	03/2020 -	04/2022	25	-
202	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	808.85	81.26	08/2022 -	09/2022	1	-
	<u>Northern Railway</u>								
203	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 695.00	750.00	290.62	12/2011 -	03/2021	111	-
204	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 -	859.00	835.35	03/2016 -	03/2021	60	-
205	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	27,949.00	20,501.11	11/2002 -	06/2022	235	-
206	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 2,010.00	2,200.00	668.77	07/2012 -	03/2024	140	-
	<u>Rail Vikas Nigam Ltd.</u>								
207	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	1,185.64 -	1,844.47	1,883.44	12/2017 -	03/2020	27	-
208	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	1,200.00	1,209.55	03/2019 -	03/2020	12	-
209	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	396.00	388.21	03/2009 03/2009	06/2020	135	135
210	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	816.55	720.70	03/2016 -	12/2020	57	-
211	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	1,402.02 -	1,100.00	1,122.87	03/2020 -	12/2020	9	-
212	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	713.48 -	2,300.00	2,131.56	03/2020 -	03/2021	12	-
213	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	948.04 -	1,500.00	1,451.81	03/2020 -	03/2021	12	-
214	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH	04/2011	1,485.85 -	1,485.85	1,196.74	12/2020 -	03/2021	3	-
215	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70 -	1,202.70	1,008.33	02/2015 -	12/2021	82	-
216	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,548.66 -	1,548.66	1,421.83	12/2021 -	03/2022	3	-
217	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	2,200.00	1,966.03	03/2020 -	03/2022	24	-
218	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	1,120.00	1,046.08	03/2019 -	06/2022	39	-
219	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	1,183.25	1,184.32	12/2020 -	12/2022	24	-

Costing Rs. 150 Crore and above

(January 2020)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
220	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA	04/2010	2,127.00 -	2,900.00	1,815.11	03/2023 -	03/2024	12	-
221	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60 -	750.56	485.98	03/2022 -	12/2024	33	-
222	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92 -	1,765.92	674.40	03/2023 -	12/2024	21	-
223	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	4,724.30	2,307.00	03/2016 -	03/2025	108	-
224	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	4,639.00	871.04	03/2016 -	03/2025	108	-
225	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00 -	16,216.00	1,941.37	12/2024 -	03/2025	3	-
226	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	2,733.86	40.13	03/2014 -	12/2025	141	-
	<u>South Central Railway</u>								
227	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 1,780.29	3,472.59	970.69	03/2000 -	03/2021	252	-
228	MANMAD-PARBHANI-NANDED- SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA	04/2017	119.73 176.17	449.39	298.13	03/2022 -	12/2022	9	-
229	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 2,120.16	2,120.16	561.18	03/2009 -	03/2023	168	-
230	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	1,160.48 1,160.48	1,160.48	340.48	03/2010 -	03/2023	156	-
231	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 2,063.03	2,063.03	880.17	03/2021 -	03/2023	24	-
232	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 3,631.00	3,631.00	678.02	03/2022 -	03/2023	12	-
233	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 1,952.68	1,952.68	329.00	03/2023 -	03/2024	12	-
234	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	2,288.70 2,643.25	2,643.25	860.07	03/2021 -	03/2024	36	-
235	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,132.77 2,132.77	2,132.77	350.17	03/2014 -	03/2024	120	-
	<u>South Eastern Railway</u>								
236	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	377.00	183.96	12/2016 08/2018	03/2020	39	19
237	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 358.68	358.68	278.34	12/2018 12/2018	08/2020	20	20
238	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 1,312.96	1,312.96	610.19	03/2020 03/2020	03/2021	12	12
239	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	1,993.24	469.79	03/2021 03/2021	12/2021	9	9

Costing Rs. 150 Crore and above

(January 2020)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>South Western Railway</u>								
240	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 644.78	890.00	461.80	03/2017 -	03/2020	36	-
241	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,156.94 1,140.94	1,140.94	918.47	03/2020 -	03/2021	12	-
242	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 1,870.41	1,870.41	1,056.97	03/2019 -	03/2021	24	-
243	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	986.30 986.30	986.30	303.05	03/2016 -	12/2023	93	-
244	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 279.54	279.54	30.62	03/2016 -	12/2023	93	-
245	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 1,382.78	1,382.78	7.35	03/2002 -	03/2024	264	-
246	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 832.47	832.47	.94	03/2016 -	03/2024	96	-
247	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 2,841.84	2,841.84	194.25	12/2018 -	12/2024	72	-
	<u>Southern Railway</u>								
248	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	2,072.50	1,471.60	02/2019 -	02/2020	12	-
249	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU	10/2013	187.26 -	231.67	167.12	04/2014 -	03/2020	71	-
250	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	980.00	683.11	03/2020 -	03/2021	12	-
251	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU	02/2015	760.00 -	1,182.31	446.00	03/2020 -	06/2021	15	-
252	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	1,567.00	-	03/2024 -	03/2026	24	-
	<u>West Central Railway</u>								
253	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH	08/2016	582.13 -	1,247.64	228.36	03/2022 -	09/2022	6	-
254	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	8,248.50	1,986.78	05/2008 -	03/2023	178	-
255	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	424.60 -	2,909.99	1,975.34	03/2021 -	03/2023	24	-
256	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH	12/2015	1,763.93 -	1,762.94	867.52	03/2020 -	03/2023	36	-
257	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH	06/2016	2,478.23 -	2,478.23	477.93	03/2022 -	03/2023	12	-
	Total		1,58,804.37 -	2,44,385.42	1,12,069.02				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>								
258	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH,MADHYA PRADESH	03/2015	511.83 -	511.83	278.88	08/2017 -	02/2020	30	-

Costing Rs. 150 Crore and above

(January 2020)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
259	AKKALKOT TO DHUDHNI - [N24001120]MoRTH,MAHARASHTRA	04/2016	211.42 -	211.42	131.85	02/2019 -	02/2020	12	-
260	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 - [N24000895]MoRTH,MADHYA PRADESH	09/2016	287.34 -	287.34	158.05	01/2019 -	03/2020	14	-
261	REHABILITATION AND UPGRADE OF HARPALPUR -SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942]MoRTH,UTTAR PRADESH	03/2016	208.50 -	208.50	141.54	11/2019 -	03/2020	4	-
262	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA	10/2016	248.83 -	248.83	91.52	03/2019 -	03/2020	12	-
263	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH,TELANGANA	01/2017	300.00 -	300.00	100.33	05/2019 -	03/2020	10	-
264	INDAPUR TO VADPALE - [N24001114]MoRTH,MAHARASHTRA	01/2017	1,202.52 1,202.52	1,202.52	635.90	12/2019 -	03/2020	3	-
265	VADPALE TO BHOGAN KHURD - [N24001115]MoRTH,MAHARASHTRA	01/2017	1,598.47 1,560.00	1,598.47	768.91	11/2019 -	03/2020	4	-
266	REHABILITATION AND UPGRADE OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH,UTTAR PRADESH	03/2016	240.30 240.00	240.30	198.06	01/2020 -	03/2020	2	-
267	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH - [N24001145]MoRTH,UTTAR PRADESH	05/2013	164.54 165.00	164.54	127.34	08/2015 -	03/2020	55	-
268	REHABILITATION AND UPGRADE OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]MoRTH,UTTAR PRADESH	03/2016	249.50 -	249.50	160.60	05/2019 -	03/2020	10	-
269	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH	03/2018	233.04 -	233.04	131.22	03/2018 -	04/2020	25	-
270	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH	02/2018	279.44 -	279.44	76.00	03/2018 -	04/2020	25	-
271	KOLHA TO NASRATPUR - [N24001111]MoRTH,MAHARASHTRA	04/2016	281.78 282.00	281.78	29.73	04/2019 -	04/2020	12	-
272	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]MoRTH,MADHYA PRADESH	11/2013	497.05 -	881.05	624.54	05/2017 -	05/2020	36	-
273	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH	03/2018	162.56 -	162.56	119.50	03/2018 -	05/2020	26	-
274	REHABILITATION AND UPGRADE OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]MoRTH,MADHYA PRADESH	11/2017	235.91 -	235.91	156.89	02/2018 -	05/2020	27	-
275	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]MoRTH,MADHYA PRADESH	11/2017	184.62 -	184.62	76.60	02/2018 -	05/2020	27	-

Costing Rs. 150 Crore and above

(January 2020)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
276	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884]MoRTH,MADHYA PRADESH	03/2018	191.21 -	191.21	78.35	11/2019 -	05/2020	6	-
277	WAKAN PALI KHOPOLI - [N24001026]MoRTH,MAHARASHTRA	01/2017	376.19 376.19	376.19	37.03	05/2019 -	05/2020	12	-
278	DEORI TO AMGAON - [N24001032]MoRTH,MAHARASHTRA	01/2017	409.62 410.00	409.62	181.78	05/2019 -	05/2020	12	-
279	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA	05/2018	171.60 -	171.60	.86	05/2018 -	05/2020	24	-
280	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH	03/2018	166.21 -	166.21	67.45	08/2018 -	06/2020	22	-
281	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]MoRTH,MADHYA PRADESH	03/2018	217.22 226.88	226.88	86.83	08/2018 -	06/2020	22	-
282	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH	11/2017	249.05 -	249.05	143.64	07/2018 -	06/2020	23	-
283	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA	10/2016	298.32 -	298.32	83.57	02/2019 -	06/2020	16	-
284	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA	01/2017	391.06 391.00	391.06	147.00	06/2019 -	06/2020	12	-
285	KARAD TO TAGAON - [N24001053]MoRTH,MAHARASHTRA	01/2017	537.81 538.00	537.81	98.97	06/2019 -	06/2020	12	-
286	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MoRTH,MAHARASHTRA	02/2017	407.19 407.00	407.19	25.00	06/2019 -	06/2020	12	-
287	MALEWADA TO CHIMUR - [N24001104]MoRTH,MAHARASHTRA	10/2016	322.55 -	322.55	184.91	06/2019 -	06/2020	12	-
288	PARLI PIMPLA DAHIGUDA - [N24001138]MoRTH,MAHARASHTRA	02/2017	205.72 205.72	205.72	30.42	06/2019 -	06/2020	12	-
289	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]MoRTH,UTTAR PRADESH	07/2016	208.88 -	208.88	95.59	10/2019 -	06/2020	8	-
290	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH,MADHYA PRADESH	02/2018	169.63 -	169.63	14.67	03/2018 -	07/2020	28	-
291	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]MoRTH,MADHYA PRADESH	03/2016	877.79 -	877.79	467.48	06/2019 -	07/2020	13	-
292	MANGAON TO DIGHI PORT - [N24001024]MoRTH,MAHARASHTRA	01/2017	457.52 457.52	457.52	277.98	07/2019 -	07/2020	12	-
293	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]MoRTH,MADHYA PRADESH	12/2015	957.54 -	957.54	573.28	02/2020 -	08/2020	6	-
294	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH	11/2015	628.45 -	628.45	300.52	01/2020 -	09/2020	8	-

Costing Rs. 150 Crore and above

(January 2020)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
295	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH	01/2017	205.05 -	205.05	85.57	03/2017 -	09/2020	42	-
296	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]MoRTH,MADHYA PRADESH	11/2017	254.17 -	254.17	157.83	02/2018 -	09/2020	31	-
297	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]MoRTH,MADHYA PRADESH	01/2017	373.82 -	373.82	143.05	09/2019 -	09/2020	12	-
298	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]MoRTH,MADHYA PRADESH	01/2016	809.16 -	809.16	353.90	07/2018 -	09/2020	26	-
299	WADI TO ASOLA - [N24001022]MoRTH,MAHARASHTRA	01/2017	363.82 363.82	363.82	92.10	09/2019 -	09/2020	12	-
300	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MoRTH,MADHYA PRADESH	11/2017	392.33 428.55	428.55	253.99	03/2018 -	09/2020	30	-
301	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH	03/2018	214.69 -	214.69	30.44	03/2018 -	12/2020	33	-
302	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]MoRTH,BIHAR	05/2014	199.98 -	199.98	153.43	08/2016 -	12/2020	52	-
303	BARASGAON TO RAHATEE - [N24001113]MoRTH,MAHARASHTRA	07/2016	289.11 290.00	289.11	33.82	09/2018 -	04/2021	31	-
304	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH,PUNJAB	03/2018	170.57 192.48	170.57	8.14	11/2020 -	05/2021	6	-
305	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA	02/2017	157.32 188.00	157.32	-	05/2019 -	05/2021	24	-
306	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH,WEST BENGAL	03/2016	160.27 213.97	213.97	20.11	08/2019 -	08/2021	24	-
307	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH,WEST BENGAL	06/2016	236.78 263.26	263.26	59.92	08/2019 -	08/2021	24	-
308	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]MoRTH,MADHYA PRADESH	11/2011	954.43 1,191.51	1,191.51	235.61	09/2015 -	10/2021	73	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
309	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH	12/2016	138.93 155.00	155.00	79.91	01/2017 -	01/2020	36	-

Costing Rs. 150 Crore and above

(January 2020)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
310	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH	03/2015	394.00 -	394.00	325.08	06/2018 -	03/2020	21	-
311	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 387.00	387.00	216.07	08/2016 -	03/2020	43	-
312	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 340.00	340.00	189.88	08/2016 -	03/2020	43	-
313	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 339.55	339.55	237.99	08/2016 -	06/2020	46	-
314	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND	02/2017	387.00 -	387.00	145.18	09/2018 -	08/2020	23	-
315	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM	05/2015	454.89 -	454.89	141.83	05/2018 05/2020	12/2020	31	7
316	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH	02/2017	168.32 168.32	168.32	40.78	04/2017 02/2018	02/2021	46	36
317	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 180.57	180.57	16.80	04/2017 02/2018	02/2021	46	36
318	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH	02/2017	216.71 216.71	216.71	25.17	04/2017 02/2018	02/2021	46	36
319	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH	02/2017	167.28 167.28	167.28	21.54	04/2017 02/2018	02/2021	46	36
320	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D - [N24000974]NHIDCL,ARUNACHAL PRADESH	02/2017	199.02 199.02	199.02	13.82	- 02/2018	02/2021	-	36
321	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D - [N24000975]NHIDCL,ARUNACHAL PRADESH	02/2017	184.88 184.88	184.88	7.68	- 02/2018	02/2021	-	36
322	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH	03/2017	284.09 284.09	284.09	96.13	04/2017 03/2018	03/2021	47	36
323	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM	01/2016	294.17 -	294.17	76.25	01/2016 02/2019	04/2021	63	26

Costing Rs. 150 Crore and above

(January 2020)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
324	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL,MANIPUR	08/2017	517.57 -	457.77	137.04	10/2018 -	10/2021	36	-
325	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM	06/2015	437.39 -	437.39	10.01	06/2018 12/2020	12/2021	42	12
326	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM	06/2015	463.49 -	463.49	26.15	06/2018 01/2021	12/2021	42	11
327	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH	01/2017	1,253.10 -	1,253.10	204.77	03/2017 -	03/2022	60	-
328	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH	02/2017	175.06 175.06	175.06	29.08	- 04/2019	04/2022	-	36
329	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL,ARUNACHAL PRADESH	02/2017	176.12 176.12	176.12	28.16	- 04/2019	04/2022	-	36
	<u>National Highways Authority Of India</u>								
330	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	323.72	232.58	08/2018 -	01/2020	17	-
331	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	639.97	331.84	10/2017 -	01/2020	27	-
332	MEERUT-BULANDSHAHAH - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 868.77	987.94	727.69	- 10/2019	02/2020	-	4
333	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 881.00	688.70	870.48	- 05/2017	02/2020	-	33
334	4 LANING OF KSHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	722.46	722.46	07/2018 12/2019	02/2020	19	2
335	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	230.00	340.21	04/2008 -	03/2020	143	-
336	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	470.01	05/2010 -	03/2020	118	-
337	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 2,967.50	2,967.50	3,990.72	11/2011 -	03/2020	100	-
338	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	2,442.58	03/2013 -	03/2020	84	-
339	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	1,132.48	02/2013 -	03/2020	85	-
340	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	3,260.65	05/2014 12/2019	03/2020	70	3
341	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	850.24	07/2013 -	03/2020	80	-

Costing Rs. 150 Crore and above

(January 2020)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
342	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI, BIHAR	05/2011	511.54 585.00	591.00	571.86	11/2013 12/2019	03/2020	76	3
343	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	1,396.18	2,894.94	09/2014 -	03/2020	66	-
344	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI, RAJASTHAN	10/2015	597.00 -	597.00	587.64	10/2017 -	03/2020	29	-
345	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI, MAHARASHTRA	01/2015	972.50 -	972.50	1,492.00	07/2017 12/2019	03/2020	32	3
346	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI, HIMACHAL PRADESH	09/2015	934.46 -	934.46	586.91	03/2018 -	03/2020	24	-
347	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI, KARNATAKA	03/2015	1,388.00 -	1,388.00	1,203.00	08/2018 -	03/2020	19	-
348	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI, MAHARASHTRA	07/2015	1,871.34 67.34	1,871.34	3,544.79	01/2018 12/2018	03/2020	26	15
349	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI, TAMIL NADU	02/2016	707.82 -	707.82	381.40	08/2018 -	03/2020	19	-
350	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI, KERALA	04/2016	804.97 -	804.97	465.05	06/2018 -	03/2020	21	-
351	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI, HARYANA	08/2016	248.97 -	248.97	249.15	05/2019 -	03/2020	10	-
352	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI, UTTAR PRADESH	06/2016	667.00 2,257.49	667.00	464.05	07/2018 -	04/2020	21	-
353	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI, UTTAR PRADESH	12/2015	667.00 3,007.86	667.00	549.07	06/2018 -	04/2020	22	-
354	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI, TAMIL NADU	09/2017	244.27 -	244.27	177.41	09/2017 -	04/2020	31	-
355	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,195.64	08/2013 -	05/2020	81	-
356	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI, MAHARASHTRA	06/2014	923.04 -	923.04	767.17	11/2016 -	05/2020	42	-
357	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI, TAMIL NADU	02/2016	641.17 -	641.17	370.82	07/2018 -	05/2020	22	-
358	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI, MAHARASHTRA	02/2017	904.16 911.07	904.16	855.25	02/2020 11/2017	05/2020	3	30
359	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI, MAHARASHTRA	03/2017	1,030.44 -	1,065.51	1,015.76	03/2020 -	05/2020	2	-
360	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI, UTTAR PRADESH	03/2017	1,989.00 2,602.09	1,989.00	892.35	03/2020 11/2017	05/2020	2	30
361	SIX LANNING OF RANASTALAM- ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI, ANDHRA PRADESH	03/2017	1,041.62 -	1,187.10	829.16	03/2020 -	05/2020	2	-

Costing Rs. 150 Crore and above

(January 2020)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
362	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	641.17	370.82	07/2016 -	05/2020	46	-
363	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 3,207.63	1,087.00	562.94	- 02/2018	05/2020	-	27
364	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,336.07	12/2013 -	06/2020	78	-
365	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,159.10	03/2014 04/2017	06/2020	75	38
366	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	2,945.00	2,467.00	04/2015 01/2017	06/2020	62	41
367	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	530.07	556.02	08/2016 -	06/2020	46	-
368	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 897.03	897.03	796.56	11/2018 07/2019	06/2020	19	11
369	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 2,182.03	815.28	520.89	06/2018 -	06/2020	24	-
370	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 2,433.38	1,027.53	601.13	06/2018 -	06/2020	24	-
371	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	1,434.00	765.31	03/2020 -	06/2020	3	-
372	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	2,136.97	1,248.94	12/2018 -	07/2020	19	-
373	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	1,177.00	702.31	03/2020 -	07/2020	4	-
374	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	174.34	225.65	03/2008 -	08/2020	149	-
375	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	329.92	06/2013 01/2019	08/2020	86	19
376	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	478.00	315.11	10/2013 -	08/2020	82	-
377	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 870.00	870.00	265.48	03/2019 03/2017	08/2020	17	41
378	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	1,310.00	563.15	03/2020 -	08/2020	5	-
379	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 988.00	1,043.28	1,035.00	03/2020 -	08/2020	5	-
380	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	1,160.64	1,068.76	03/2020 -	08/2020	5	-

Costing Rs. 150 Crore and above

(January 2020)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
381	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH	06/2017	648.33 -	306.00	157.33	06/2017 -	08/2020	38	-
382	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	1,227.87	387.40	09/2017 -	08/2020	35	-
383	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	2,913.83	07/2015 12/2019	09/2020	62	9
384	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	727.00	524.15	05/2018 -	09/2020	28	-
385	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	504.00	241.74	05/2018 04/2019	09/2020	28	17
386	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	1,176.37	207.17	08/2017 -	09/2020	37	-
387	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	2,898.41	06/2014 09/2017	10/2020	76	37
388	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	1,364.18	03/2013 11/2019	11/2020	92	12
389	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	701.40	29.48	03/2019 -	11/2020	20	-
390	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	870.00	36.30	03/2019 -	11/2020	20	-
391	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	1,373.28	571.96	03/2020 -	11/2020	8	-
392	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	1,071.00	610.87	03/2017 05/2018	11/2020	44	30
393	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	964.17	390.91	10/2017 -	11/2020	37	-
394	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	1,655.01	1,867.51	08/2016 -	12/2020	52	-
395	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	2,168.66	704.09	06/2019 -	12/2020	18	-
396	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	322.09	77.53	04/2018 -	12/2020	32	-
397	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 1,008.00	1,108.00	1,399.33	08/2019 -	12/2020	16	-
398	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	207.00	34.77	- 03/2020	12/2020	-	9

Costing Rs. 150 Crore and above

(January 2020)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
399	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	990.61	397.89	09/2017 -	01/2021	40	-
400	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT	03/2018	2,702.05 -	2,043.00	-	- 05/2018	01/2021	-	32
401	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	400.25	64.89	03/2019 -	02/2021	23	-
402	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT	06/2017	1,958.88 1,993.81	1,993.81	1,116.85	06/2020 02/2018	02/2021	8	36
403	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,822.59	08/2013 -	03/2021	91	-
404	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	2,510.04	358.51	08/2019 -	03/2021	19	-
405	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	446.17	38.97	03/2019 -	03/2021	24	-
406	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	1,420.00	532.31	03/2020 -	03/2021	12	-
407	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 1,073.10	1,005.08	-	- 03/2019	03/2021	-	24
408	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA	01/2018	621.00 565.02	621.00	383.83	- 10/2018	04/2021	-	30
409	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH	03/2018	1,532.62 2,499.00	2,499.00	730.93	03/2021 -	04/2021	1	-
410	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	227.77	11.00	03/2020 -	05/2021	14	-
411	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	1,232.76	314.14	09/2017 -	05/2021	44	-
412	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	476.56	1.49	07/2017 11/2020	06/2021	47	7
413	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	686.65	114.36	- 07/2020	06/2021	-	11
414	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	953.09	224.11	- 05/2020	06/2021	-	13

Costing Rs. 150 Crore and above

(January 2020)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
415	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	668.86	175.29	- 05/2020	06/2021	-	13
416	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	686.65	105.69	- 03/2020	06/2021	-	15
417	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64 1,687.00	1,437.64	564.11	- 12/2018	07/2021	-	31
418	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	756.27	193.96	03/2020 -	08/2021	17	-
419	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA	01/2018	607.00 512.99	607.00	187.53	- 02/2019	08/2021	-	30
420	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	2,485.93	596.94	06/2020 -	09/2021	15	-
421	SIX-LANING OF BANGALORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 2,190.00	2,400.00	1,740.36	- 05/2019	11/2021	-	30
422	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	950.64	102.51	08/2017 -	02/2022	54	-
	Total		1,21,421.72 -	1,26,563.16	85,150.76				
	<u>TELECOMMUNICATIONS</u>								
	<u>Department Of Telecommunication</u>								
423	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	24,664.00	12,146.00	07/2015 -	05/2020	58	-
	Total		13,334.00 -	24,664.00	12,146.00				
	<u>URBAN DEVELOPMENT</u>								
	<u>Ahmedabad Metro Rail</u>								
424	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT	11/2014	10,773.00 -	10,773.00	6,532.69	12/2018 -	07/2020	19	-
	<u>Bangalore Metro Rail Corporation Limited</u>								
425	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	26,405.14	499.85	02/2019 -	03/2020	13	-
	<u>Central Public Works Department</u>								
426	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	159.35	08/2016 -	01/2020	41	-
427	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	165.23	100.81	10/2012 -	03/2020	89	-

Costing Rs. 150 Crore and above

(January 2020)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
428	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB	02/2014	388.00 500.18	490.00	442.51	05/2017 -	03/2020	34	-
429	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]CPWD,PUNJAB	08/2016	294.00 350.69	350.69	219.60	04/2019 -	05/2020	13	-
430	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD,TAMIL NADU	12/2015	209.00 -	209.00	150.71	10/2019 -	07/2020	9	-
431	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI	10/2016	248.20 -	248.20	52.95	04/2018 02/2020	08/2020	28	6
432	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN	12/2016	549.31 559.47	559.47	373.45	07/2019 03/2020	08/2020	13	5
433	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	97.70	03/2016 -	09/2020	54	-
434	RESIDENTIAL QUATERS FOR HAL,BANGLORE - [N28000103]CPWD,KARNATAKA	12/2016	246.31 -	246.31	85.43	02/2020 -	09/2020	7	-
435	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR	02/2014	216.69 -	216.69	52.00	03/2015 -	10/2020	67	-
436	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI	06/2015	197.33 -	197.33	67.09	04/2019 -	12/2020	20	-
437	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT - [N28000139]CPWD,PONDICHERRY	03/2018	195.00 -	195.00	-	09/2020 -	01/2021	4	-
438	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB - [N28000120]CPWD,PUNJAB	01/2018	430.00 387.83	387.83	124.24	05/2020 -	02/2021	9	-
439	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	2,000.00	436.20	10/2019 -	03/2021	17	-
440	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	498.99	118.00	06/2017 -	03/2021	45	-
441	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST) - [N28000112]CPWD,KERALA	09/2017	150.29 -	150.29	21.82	03/2020 11/2020	03/2021	12	4
442	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 -	392.00	13.90	- 08/2020	03/2021	-	7
443	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA	10/2016	209.84 -	209.84	70.43	03/2020 -	05/2021	14	-

Costing Rs. 150 Crore and above

(January 2020)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>Hindustan Steelwork Construction Limited</u>								
444	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72	-
	<u>Kochi Metro Rail Corporation Ltd</u>								
445	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 5,687.79	6,218.14	5,817.11	07/2017 -	03/2020	32	-
	<u>Mumbai Metro Rail Corporation Ltd</u>								
446	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	05/2020	64	-
	<u>National Building Construcion Corporation Ltd</u>								
447	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI	06/2012	4,264.00 4,720.73	4,720.73	4,553.13	11/2019 03/2020	05/2020	6	2
	Total		76,650.95 -	79,054.31	20,640.18				
	<u>WATER RESOURCES</u>								
	<u>Polavaram Project Authority</u>								
448	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA,ANDHRA PRADESH	02/2009	10,151.04 55,548.87	55,548.87	32,535.80	03/2020 11/2019	12/2021	21	25
	Total		10,151.04 -	55,548.87	32,535.80				
	<u>COMMERCE AND INDUSTRY</u>								
	<u>Delhi Mumbai Industrial Corridor</u>								
449	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]DMIC,MULTI STATE	09/2011	12,579.09 -	12,579.09	778.93	09/2019 -	09/2020	12	-
	<u>India International Convention And Expo Centre</u>								
450	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]IICC,DELHI	11/2017	4,773.00 -	5,178.00	1,309.65	12/2019 -	09/2020	9	-
	Total		17,352.09 -	17,757.09	2,088.58				
	<u>HUMAN RESOURCE DEVELOPMENT</u>								
	<u>Rail India Technical And Economic Service</u>								
451	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]RITES,MEGHALAYA	09/2013	484.32 -	626.26	-	09/2014 -	12/2020	75	-
	Total		484.32 -	626.26	.00				
	Grand Total		7,10,612.79	9,01,066.51	4,56,961.53				

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2020)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	03/2023	12320	75
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	09/2021	11459	69
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2021	3492	133
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	NPCIL	03/2013	11/2020	11/2023	39849	36

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
5	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	AAI	01/2016	03/2020	12/2020	219.91	9
6	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPORT	AAI	11/2016	04/2020	12/2020	233.38	8
7	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	AAI	06/2018	02/2022	08/2022	2467	6
8	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2020	314.61	21

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
9	RANIGANJ MASTER PLAN	ECL	08/2009	08/2019	08/2024	2661.73	60
10	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1	SCCL	03/2017	03/2019	03/2022	413.84	36
11	KALYANIKHANI OPENCAST PROJECT	SCCL	07/2012	07/2016	03/2020	417.33	44
12	BAROUD OC EXPANSION (RCE)- 3MTY	SECL	04/2012	03/2016	03/2020	258.56	48
13	JALAGAM VENGALA RAO OCP-II	SCCL	07/2011	03/2015	03/2021	447.06	72
14	RAJRAPPA RCE OCP (3.0 MTY)	CCL	12/2009	03/2016	03/2021	510.85	60
15	KANIHA OCP, MCL, (10.0 MTY)	MCL	12/2007	03/2013	03/2022	457.77	108
16	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2009	03/2014	03/2021	321.5	84
17	BHUBANESWARI OCP, MCL (20.0 MTY)	MCL	12/2007	03/2017	03/2021	490.1	48
18	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	03/2012	03/2021	207.28	108
19	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2022	479.53	108
20	RKP OCP PHASE-I	SCCL	03/2010	03/2015	03/2020	209.78	60

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
21	BALRAM OCP EXTENSION, MCL 8.00 MTY	MCL	12/2007	03/2010	03/2022	172.08	144
22	MOONIDIH XV SEAM UG	BCCL	08/2011	04/2015	04/2022	1230.27	84
23	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2021	163.51	120
24	TAPIN OCP (2.5 MTY)	CCL	08/2008	03/2012	03/2021	264.68	108
25	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2021	162.46	84
26	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2024	249.03	144
27	KISTARAM OCP	SCCL	11/2010	03/2015	03/2021	242.29	72
28	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2020	178.44	72
29	KAMPTEE DEEP OC MINE	WCL	11/2015	03/2021	03/2024	277.65	36
30	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	ECL	08/2012	03/2018	10/2020	1055.05	31
31	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	MCL	05/2014	03/2019	03/2024	479.15	60
32	JAGANNATH RE-ORGANISATION OC.(6.00 MTY)	MCL	05/2014	03/2019	03/2021	337.66	24
33	KULDA EXPN OC. (5.00 MTY)	MCL	06/2014	03/2018	03/2021	289.03	36
34	AMERA OC RCE	SECL	02/2015	03/2018	03/2020	335.97	24
35	MADHUBAND NLW WASHERY	BCCL	08/2010	05/2014	05/2020	289.45	72
36	PATHERDIH NLW WASHERY	BCCL	10/2012	04/2014	03/2020	269.82	71
37	KAKATIYAKHANI OPENCAST-2 PROJECT	SCCL	05/2015	03/2019	03/2020	397.09	12
38	ADASA UG TO OC	WCL	08/2015	03/2023	03/2024	288.9	12
39	KULDA OCP (MAHANADI COALFIELDS LTD)	MCL	01/2005	03/2010	03/2020	302.96	120
40	KOYAGUDEM OPENCAST PROJECT	SCCL	10/2015	03/2018	03/2020	426.79	24
41	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	60
42	MAGADH OC 20 MTY (CCL)	CCL	08/2008	07/2012	03/2022	706.4	116
43	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2023	418.97	132

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
44	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	03/2020	5907.11	51
45	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2021	162.76	72
46	RG OC -III EXTENSION (PHASE -II) PROJECT	SCCL	06/2012	06/2015	03/2020	365.01	57
47	RFR OF MANUGURU OC PROJECT	SCCL	11/2012	03/2016	03/2020	430.45	48

COMMERCE AND INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
48	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	IICC	11/2017	12/2019	09/2020	4773	9
49	DELHI MUMBAI INDUSTRIAL CORRIDOR	DMIC	09/2011	09/2019	09/2020	12579.09	12

FERTILISERS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
50	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL	NFL	01/2018	11/2019	05/2020	239.81	6
51	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA	NFL	01/2018	11/2019	05/2020	218.83	6

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
52	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	HITES	07/2016	04/2020	10/2020	785	6
53	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	HSCC	07/2016	02/2018	03/2020	152.95	25
54	AIIMS - OPD(NEW)	HSCC	08/2014	05/2017	01/2020	293.65	32
55	NEIGRIHMS SHILLONG MEGHALYA	HSCC	10/2016	05/2018	07/2020	363.99	26
56	AIIMS - MOTHER AND CHILD BLOCK	HSCC	12/2013	05/2017	06/2020	204.44	37
57	LHMC NEW DELHI-RE-DEVELOPMENT	HSCC	02/2013	11/2013	09/2020	414.11	82
58	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH	HSCC	08/2017	03/2019	03/2020	272.19	12
59	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA	HSCC	08/2017	03/2019	03/2020	274.19	12
60	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	HSCC	08/2017	03/2019	07/2020	355.15	16

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2020)

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
61	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	BHEL	08/2016	09/2019	03/2020	1554	6

HUMAN RESOURCE DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
62	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	MITES	09/2013	09/2014	12/2020	484.32	75

MINES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
63	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU	NALCO	09/2017	06/2019	12/2020	166.62	18
64	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	NALCO	12/2014	04/2021	12/2022	5540	20

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
65	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY	IOCL	10/2018	02/2020	01/2021	598	11
66	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY	IOCL	01/2019	01/2021	08/2021	909	7
67	RE-LIQUIFIED NATURAL GAS	CPCL	08/2017	08/2020	02/2021	421	6
68	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	IOCL	12/2017	10/2020	08/2021	466.43	10
69	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	02/2022	1112	32
70	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA	HPCL	06/2017	06/2020	09/2021	249.26	15
71	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE	HPCL	06/2017	06/2020	09/2021	161.5	15
72	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	IOCL	04/2018	02/2020	12/2020	206.63	10
73	BS-VI PROJECT AT PANIPAT REFINERY	IOCL	12/2017	07/2019	02/2020	3529	7
74	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE	IOCL	10/2017	02/2020	10/2020	906	8
75	REVAMPING OF FACILITIES AT VIZAG TERMINAL	IOCL	04/2018	04/2022	02/2023	355	10
76	HALDIA LPG IMPORT FACILITY	BPCL	03/2015	10/2018	02/2020	694	16
77	VISAKH REFINERY MODERNISATION PROJECT	HPCL	07/2016	07/2020	07/2022	20928	24
78	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR), CACHAR, ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	IOCL	06/2016	08/2019	12/2020	423	16

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
79	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	ONGC	11/2015	03/2019	05/2020	650.82	14
80	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	ONGC	03/2016	06/2020	08/2021	34012	14
81	ENNORE THIRUVALUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	02/2021	4497	26
82	BSVI UPGRADATION	MANGALORE REFI	09/2016	12/2019	03/2021	1810	15
83	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II	OIL	09/2016	12/2019	06/2020	571.66	6
84	MMPL PIPELINE REROUTING PROJECT	BPCL	04/2013	12/2019	07/2020	449.58	7
85	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY	BPCL	02/2016	02/2020	10/2020	3313	8
86	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA	ONGC	01/2015	12/2017	03/2020	4619.94	27
87	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	05/2020	3190.69	25
88	SITARGANJ LPG PROJECT	IOCL	02/2017	02/2020	10/2020	160.1	8
89	LPG BP PROJECT KHORDHA	IOCL	12/2016	12/2019	07/2021	161.59	19
90	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	02/2022	2915	110
91	SEA WATER DESALINATION PLANT	MANGALORE REFI	11/2017	03/2020	11/2020	581	8
92	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	OIL	07/2011	03/2017	06/2020	352.56	39
93	PARADIP LPG IMPORT FACILITY	IOCL	01/2015	07/2018	10/2020	690	27
94	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III	ONGC	11/2014	04/2019	03/2020	6068.8	11
95	DAMAN DEVELOPMENT PROJECT	ONGC	08/2014	05/2019	03/2020	6086.08	10
96	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY	ONGC	08/2015	03/2019	05/2020	2818.88	14
97	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	02/2020	861.79	81
98	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	03/2020	2059.63	60
99	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	02/2020	4588.29	18
100	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	GAIL	04/2016	04/2018	02/2020	327.78	22
101	IRUGUR-DEVANGONTHI POL PIPELINE	BPCL	11/2012	02/2017	10/2021	678	56

DOA -> Date of Approval

DOC -> Date of Commissioning

486

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
102	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	IOCL	05/2016	01/2021	10/2021	348	9
103	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY	IOCL	05/2016	01/2019	06/2020	429	17
104	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)	ONGC	02/2017	05/2021	12/2021	4006.83	7
105	KHARAGPUR LPG BOTTLING PLANT	IOCL	04/2017	04/2020	03/2021	163.02	11
106	GRASS ROOT TERMINAL AT MALKAPUR	IOCL	12/2018	04/2022	03/2023	611	11
107	FUEL QUALITY UPGRADATION (NSU,NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY	IOCL	06/2017	10/2019	05/2020	951.64	7

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
108	DURGAPUR PP-III (2X20 MW) - NSPCL	NTPC	12/2016	11/2018	08/2020	529.68	21
109	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/	PGCIL	02/2017	02/2019	03/2020	322.3	13
110	SYTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	02/2020	487.49	68
111	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	08/2021	8692.97	118
112	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	10/2017	03/2020	11846	29
113	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	NTPC	01/2016	11/2020	09/2021	10598.98	10
114	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	PGCIL	03/2016	01/2018	03/2020	808.63	26
115	EASTERN REGION STRENGTHENING SCHEME-XV	PGCIL	04/2016	04/2018	01/2020	454.11	21
116	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D	PGCIL	05/2016	05/2019	02/2020	3519.59	9
117	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II)	PGCIL	10/2016	01/2019	03/2020	408.46	14
118	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	PGCIL	10/2016	04/2019	01/2020	608.24	9
119	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	03/2022	14366.58	33
120	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	11/2022	1381.84	38
121	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP)	PGCIL	01/2015	10/2017	03/2020	871.62	29
122	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII	PGCIL	01/2015	07/2017	01/2020	203.28	30

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
123	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	PGCIL	03/2015	03/2018	03/2020	197.4	24
124	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	PGCIL	03/2015	05/2017	03/2020	1394.52	34
125	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	07/2012	09/2020	5353	98
126	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2022	2491.58	114
127	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	06/2020	2496.9	126
128	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT	PGCIL	05/2017	09/2018	03/2020	175.64	18
129	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY	PGCIL	05/2017	07/2019	03/2020	186.17	8
130	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B)	PGCIL	05/2017	02/2019	05/2020	445.89	15
131	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	06/2021	12964.6	37
132	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	02/2017	06/2020	9750.89	40
133	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2021	3919.59	147
134	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	08/2023	6285.33	155
135	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	03/2020	4824.12	89
136	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	01/2018	03/2020	11638.55	26
137	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	PGCIL	12/2015	04/2019	01/2020	3654	9
138	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	03/2022	11130.19	103
139	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	02/2020	1364.52	46
140	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	PGCIL	01/2014	04/2016	03/2020	374.63	47
141	EASTERN REGION STRENGTHENING SCHEME-XII	PGCIL	05/2014	11/2016	03/2020	522.29	40
142	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2021	2978.48	105
143	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH	PGCIL	06/2014	03/2018	03/2020	5151.37	24
144	TANDA TPP STAGE-II (2X660 MW)	NTPC	09/2014	07/2019	09/2020	9188.98	14
145	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	12/2018	08/2020	12532.44	20

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
146	EASTERN REGION STRENGTHENING SCHEME XVII(PART B)	PGCIL	02/2017	06/2019	03/2020	235.53	9
147	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL	NTPC	05/2016	12/2018	08/2020	1885.13	20
148	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT	PGCIL	12/2017	06/2019	03/2020	193.14	9
149	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	12/2020	5111.33	24
150	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	12/2020	4754.42	24

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
151	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM	WR	04/2017	03/2020	03/2021	691.84	12
152	ANUPPUR-KATNI	SECR	04/2015	12/2021	03/2023	1370	15
153	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	03/2023	229	15
154	MAU-GHAZIPUR-TARIGHAT NEW LINE	RVNL	04/2015	03/2023	12/2024	1765.92	21
155	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	03/2021	713.48	12
156	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	03/2021	948.04	12
157	RAIPUR - TITLAGARH - DOUBLING	RVNL	03/2007	03/2020	12/2020	1402.02	9
158	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	06/2022	942.95	39
159	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	RVNL	03/2012	12/2020	12/2022	1183.25	24
160	KATNI-BINA 3RD LINE (263 KM)	WCR	06/2016	03/2022	03/2023	2478.23	12
161	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	09/2022	582.13	6
162	RAMNA - SINGRAULI DOUBLING	ECR	08/2015	03/2020	03/2021	2436.21	12
163	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	03/2022	548	24
164	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	09/2021	569.63	18
165	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	03/2019	03/2020	314	12
166	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2020	632.68	57

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
167	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	ER	04/1987	03/2006	03/2025	406.99	228
168	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	03/2025	915.98	36
169	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3	ER	04/2001	03/2016	03/2025	923.52	108
170	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	ER	04/2005	03/2017	03/2025	595.51	96
171	KATNI - SINGRAULI DOUBLING PROJECT	WCR	12/2015	03/2020	03/2023	1763.93	36
172	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR	NFR	04/1983	03/2019	03/2020	297.32	12
173	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2023	1045.2	168
174	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	03/2025	1188.91	72
175	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	03/2024	607.09	133
176	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	12/2017	03/2020	1185.64	27
177	RAMGANJMUNDI-BHOPAL (NL), WCR	WCR	04/2001	03/2021	03/2023	424.6	24
178	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	12/2021	1202.7	82
179	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	06/2020	133.41	135
180	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	06/2024	810.78	36
181	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI	SR	09/2007	02/2019	02/2020	724.69	12
182	BARDHAMAN-KATWA (GC)	ER	04/2007	12/2010	03/2025	1106.62	171
183	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	03/2022	2393.47	96
184	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	03/2020	477.88	96
185	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	03/2010	03/2023	1160.48	156
186	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	03/2025	2913.51	108
187	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	03/2023	3503.69	12
188	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	ER	04/2010	03/2016	03/2025	277.28	108
189	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE	ER	04/2010	03/2017	03/2025	365.17	96

DOA -> Date of Approval

DOC -> Date of Commissioning

490

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	WITH MM BARUIPARA FURFURA NL						
190	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS)	ER	04/2010	11/2018	03/2021	157.94	28
191	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	03/2022	792.89	12
192	HANSDIHA-GODDA NL	ER	04/2011	03/2020	03/2021	542.18	12
193	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY	ER	04/2011	03/2017	03/2026	299.6	108
194	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL	ER	04/2010	03/2005	03/2025	494.54	240
195	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	02/2012	03/2025	499.96	157
196	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL	ER	04/2009	03/2014	03/2025	257.42	132
197	3RD LINE BETWEEN BHUSAWAL-JALGAON	CR	04/2011	03/2019	03/2020	184.06	12
198	WARDHA-SEWAGRAM NGP 3RD LINE	CR	04/2012	03/2022	03/2024	540.02	24
199	BAGALKOT-KUDACHI NL	SWR	04/2010	03/2016	12/2023	986.3	93
200	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	03/2023	03/2024	1856.95	12
201	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	03/2021	287	111
202	SHIMOGA-HARIHAR NL	SWR	04/2011	03/2016	03/2024	832.47	96
203	NADIKUDE-SRI KALAHASTI	SCR	04/2011	03/2021	03/2024	2288.7	36
204	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	SCR	04/2008	03/2014	03/2024	2132.77	120
205	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	RVNL	04/2010	03/2023	03/2024	2127	12
206	GADAG-WADI NL	SWR	04/2013	12/2018	12/2024	2841.84	72
207	MARIKUPPAM - KUPPAM	SWR	04/2012	03/2016	12/2023	279.54	93
208	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	03/2022	2271.5	12
209	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	03/2021	495.44	204
210	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2023	247.66	178
211	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	03/2020	324.73	96

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
212	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	03/2021	1180.19	147
213	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	06/2024	2923.13	183
214	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2022	4454.17	132
215	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	03/2020	385.2	12
216	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	03/2020	532.87	12
217	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	10/2021	2326.52	79
218	MUMBAI URBAN TRANSPORT PROJECT PHASE- II	MRTPT	04/2008	03/2014	03/2021	5300	84
219	DAUSA-GANGAPUR CITY(NL), NWR	NWR	02/1997	02/2019	06/2021	410.08	28
220	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	03/2024	450	140
221	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	06/2022	2500	235
222	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	03/2025	3951.98	108
223	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	141
224	MUNEERABAD-MAHABOOBNAGAR(NL), SCR	SCR	04/1997	03/2000	03/2021	1723	252
225	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	04/2020	01/2021	511.86	9
226	BANGLORE - SATYAMANGALAM (NL)(SWR)	SWR	04/1996	03/2002	03/2024	1382.78	264
227	TIRUCHIRAPPALI-NAGORE- KARAIKKAL(SR)(GC)	SR	09/1995	03/2020	03/2021	303.98	12
228	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	WR	04/2008	03/2012	03/2022	318.24	120
229	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	03/2021	829.74	12
230	VIJAYWADA-GUDUGOLANU-BHIMAVARAM- NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	03/2022	1503.71	24
231	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	03/2022	1111.99	37
232	BHADRAK - NERGUNDI 3RD LINE	ECOR	03/2013	10/2020	03/2023	843.04	29
233	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	03/2020	03/2023	1160	36
234	SAMBALPUR - ANGUL RLY. ELECTRIFICATION	ECOR	03/2012	03/2020	03/2021	155.81	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
235	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	SER	04/2012	12/2016	03/2020	148.77	39
236	HUBLI- CHIKJAJUR	SWR	03/2015	03/2020	03/2021	1156.94	12
237	PHULERA - DIGANA DOUBLING	NWR	05/2015	03/2020	04/2022	600	25
238	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	03/2021	1614.59	24
239	HAJIPUR - BACHAWARA	ECR	05/2015	03/2019	02/2021	678.54	23
240	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	01/2020	295	12
241	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	MRTPT	03/2013	03/2016	06/2021	4874.58	63
242	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	12/2019	02/2021	246.08	14
243	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	WR	04/2007	03/2022	03/2023	1640.04	12
244	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	03/2022	320.66	36
245	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	03/2021	03/2022	1037.15	12
246	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	12/2024	2912.96	33
247	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTISURGARH-UDAIPUR	NWR	04/2013	03/2020	12/2020	420.18	9
248	AJMER-BANGURGRAM	NWR	04/2011	11/2019	12/2020	213.39	13
249	ALWAR-BANDIKUI DOUBLING	NWR	04/2013	02/2019	02/2020	242.09	12
250	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	03/2025	651	120
251	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	12/2018	08/2020	258.2	20
252	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	CR	02/2015	03/2022	03/2023	1272.19	12
253	MANMAD - JALGAON - 3RD LINE (160 KM)	CR	02/2016	03/2022	03/2024	1035.16	24
254	WARDHA - NAGPUR - 4TH LINE (76 KM)	CR	02/2016	03/2023	03/2024	637.95	12
255	GUNTUR-GUNTAKAL	SCR	04/2016	03/2022	03/2023	3631	12
256	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM	SR	10/2013	04/2014	03/2020	187.26	71
257	JAGADALPUR-KORAPUT DOUBLING	ECOR	04/2015	03/2022	03/2023	1547.38	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
258	KOTTAVALSA - KORAPUT DOUBLING	ECOR	04/2015	03/2022	03/2024	2499.71	24
259	KORAPUT - SINGAPUR ROAD DOUBLING	ECOR	04/2015	03/2022	03/2025	2361.74	36
260	KIUL - GAYA DOUBLING PROJECT	ECR	12/2015	03/2020	10/2021	1200.2	19
261	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	ECR	12/2015	03/2020	12/2021	1491.47	21
262	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	03/2022	701.61	40
263	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	ECOR	04/2015	12/2018	03/2023	1172.92	51
264	KAZIPET-BALHRSHA	SCR	04/2015	03/2021	03/2023	2063.03	24
265	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	03/2021	969.83	12
266	BONDAMUNDA RANCHI DOUBLING	SER	03/2016	03/2021	12/2021	1724.2	9
267	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	RVNL	04/2015	03/2022	12/2024	943.6	33
268	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	03/2030	1027.4	324
269	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	03/2020	927.01	12
270	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL	IRCON	04/2016	03/2020	06/2023	5200	39
271	KARAILA ROAD - SHAKTINAGAR DOUBLING	ECR	08/2015	03/2019	03/2021	528.57	24
272	MULTI MODAL LOGISTICS PARK AT KATHUWAS	CCOI	01/2011	03/2018	03/2020	493.17	24
273	MULTI MODAL LOGISTICS PARK AT BARHI	CCOI	12/2015	03/2019	03/2020	346.32	12
274	MULTI MODAL LOGISTICS PARK AT TIHI	CCOI	12/2015	03/2019	02/2020	174	11
275	MULTI MODAL LOGISTICS PARK AT KAKINADA	CCOI	08/2016	03/2019	12/2020	234.5	21
276	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	SCR	04/2017	03/2022	12/2022	119.73	9
277	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM)	SR	02/2017	03/2024	03/2026	1567	24
278	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	SR	02/2015	03/2020	06/2021	760	15
279	INDARA - DOHRIGHAT GAUGE CONVERSION.	NER	04/2016	04/2016	06/2020	213	50
280	NANPARA - NEPALGANJ GAUGE CONVERSION.	NER	04/2017	04/2017	10/2022	150	66

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
281	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION	NER	04/2017	04/2017	01/2020	622.5	33
282	ETAH - KASGANJ - NEW LINE	NER	04/2017	04/2017	04/2022	276.9	60
283	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING.	NER	04/2016	12/2019	04/2021	1177.96	16
284	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	03/2022	744.04	12
285	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM	ECR	04/2016	03/2021	03/2022	731.64	12
286	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	12/2020	585.93	22
287	JHARSUGUDA-BILASPUR 4TH LINE	SECR	04/2015	03/2021	03/2023	1973	24
288	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	03/2020	644.78	36
289	JALANDHAR-PATHANKOT-JAMMU TAWI	NR	03/2002	03/2016	03/2021	625	60
290	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	IRCON	04/2013	09/2018	03/2021	3055	30
291	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	WR	02/1991	03/2019	03/2020	551.51	12
292	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	12/2022	2288	9
293	INDORE-DEWAS-UJJAIN (80 KMS)	WR	04/2016	06/2020	06/2021	700	12

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
294	R AND U FROM KM 385.00 TO KM 420.000 TO 2- LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404	MORTH	12/2016	10/2019	04/2020	209.1	6
295	DEORI TO AMGAON	MORTH	01/2017	05/2019	05/2020	409.62	12
296	KARAD TO TAGAON	MORTH	01/2017	06/2019	06/2020	537.81	12
297	KARAD PATAN CHIPLUN GUHAGAR	MORTH	02/2017	06/2019	06/2020	407.19	12
298	MALEWADA TO CHIMUR	MORTH	10/2016	06/2019	06/2020	322.55	12
299	KOLHA TO NASRATPUR	MORTH	04/2016	04/2019	04/2020	281.78	12
300	BARASGAON TO RAHATEE	MORTH	07/2016	09/2018	04/2021	289.11	31
301	AKKALKOT TO DHUDHNI	MORTH	04/2016	02/2019	02/2020	211.42	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
302	PARLI PIMPLA DAHIGUDA	MoRTH	02/2017	06/2019	06/2020	205.72	12
303	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH	MoRTH	05/2013	08/2015	03/2020	164.54	55
304	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P	NHAI	06/2017	06/2020	09/2021	2485.93	15
305	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT	NHAI	06/2017	06/2020	02/2021	1958.88	8
306	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA	MoRTH	03/2018	11/2018	05/2020	504.19	18
307	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 0	MoRTH	03/2016	05/2016	07/2020	995.09	50
308	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P	MoRTH	01/2018	08/2018	08/2020	418.03	24
309	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD	MoRTH	08/2016	01/2017	04/2020	350.61	39
310	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216	MoRTH	03/2016	09/2016	03/2020	444.84	42
311	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT	MoRTH	01/2016	08/2016	03/2020	348.95	43
312	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2	MoRTH	11/2016	08/2017	02/2020	376.25	30
313	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216	MoRTH	01/2017	09/2017	12/2020	263.45	39
314	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH	MoRTH	01/2017	01/2018	01/2020	576.48	24
315	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	MoRTH	11/2010	03/2011	12/2020	624.41	117
316	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MoRTH	08/2010	10/2010	06/2021	193.69	128
317	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	MoRTH	08/2010	10/2010	06/2020	195.04	116
318	FOUR LANNING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	NHAI	03/2016	07/2016	05/2020	641.17	46
319	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	NHAI	08/2017	08/2017	02/2022	950.64	54
320	FOUR LANNING OF CHOLOPURAM-THANJAVUR	NHAI	08/2017	08/2017	09/2020	1176.37	37
321	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	NHAI	07/2017	07/2017	06/2021	476.56	47
322	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40)	NHAI	06/2017	06/2017	08/2020	648.33	38
323	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM	NHAI	10/2017	10/2017	01/2020	639.97	27

DOA -> Date of Approval

DOC -> Date of Commissioning

496

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	MUBARAKPUR TO BIAORA FROM KM 124.						
324	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540	NHAI	10/2017	10/2017	11/2020	964.17	37
325	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	05/2021	1124.11	44
326	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69	NHAI	09/2017	09/2017	01/2021	990.61	40
327	4-LANNING OF OTTANCHATRAM BYPASS	NHAI	09/2017	09/2017	04/2020	244.27	31
328	4-LANNING OF STHIYATHOPU-CHOLOPURAM	NHAI	09/2017	09/2017	08/2020	1227.87	35
329	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES	MoRTH	03/2015	10/2015	01/2020	271.45	51
330	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	NHIDCL	05/2015	05/2018	12/2020	454.89	31
331	4 LANING OF JORHAT TO JHANJHI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	NHIDCL	06/2015	06/2018	12/2021	437.39	42
332	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5	NHIDCL	06/2015	06/2018	12/2021	463.49	42
333	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	NHIDCL	03/2015	06/2018	03/2020	394	21
334	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	MoRTH	11/2013	05/2017	05/2020	497.05	36
335	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400	MoRTH	11/2015	01/2020	09/2020	628.45	8
336	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93	MoRTH	12/2015	02/2020	08/2020	957.54	6
337	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200	MoRTH	03/2015	08/2017	02/2020	511.83	30
338	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) 0	NHIDCL	01/2016	01/2016	04/2021	294.17	63
339	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	MoRTH	11/2011	09/2015	10/2021	954.43	73
340	GWALIOR-JHANSI, NH-75	NHAI	12/2003	12/2009	03/2020	604	123
341	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	NHAI	07/2010	07/2015	09/2020	1987	62
342	PATNA-MUZZAFFARPUR	NHAI	08/2010	02/2013	03/2020	671.3	85
343	4-LANNING OF CHAPRA-HAJIPUR	NHAI	01/2011	07/2013	03/2020	575	80
344	2 LANNING OF MUZZAFFARPUR - SONBARSA	NHAI	05/2011	11/2013	03/2020	511.54	76
345	SRINAGAR TO BANIHAL	NHAI	06/2011	06/2014	10/2020	1100.7	76
346	DELHI/ HARYANA BORDER TO ROHTAK	NHAI	04/2007	05/2010	03/2020	486	118

DOA -> Date of Approval

DOC -> Date of Commissioning

497

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
347	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	03/2020	1108	100
348	PUNE-SATARA(NH-4)	NHAI	10/2010	03/2013	03/2020	1724.55	84
349	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	NHAI	09/2011	12/2013	06/2020	1250	78
350	KANDLA - MUNDRA PORT	NHAI	01/2011	07/2013	11/2020	953.88	88
351	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	06/2020	2848	75
352	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	NHAI	11/2011	05/2014	03/2020	1535	70
353	MUZAFFARNAGAR-HARIDWAR	NHAI	09/2011	03/2013	11/2020	754	92
354	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	08/2013	05/2020	1078.84	81
355	4-LANING OF BRAHAMPUR-FARAKA	NHAI	02/2011	08/2013	03/2021	998.79	91
356	6-LANING OF DHANKUNI-KHARAGPUR SECTION	NHAI	04/2012	09/2014	03/2020	1396.18	66
357	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	06/2020	1928.22	62
358	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA	NHAI	11/2012	08/2016	06/2020	530.07	46
359	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	NHAI	01/2015	07/2017	03/2020	972.5	32
360	4-LANING OF SOLAPUR - MAHARASHTRA/KARNATKA SECTION	NHAI	06/2014	11/2016	05/2020	923.04	42
361	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	NHAI	05/2014	08/2016	12/2020	1655.01	52
362	FOUR LANING OF HOSPET - CHITRADURGA	NHAI	03/2015	08/2018	03/2020	1388	19
363	FOUR LANING OF AURANGABAD - YEDISHI	NHAI	07/2015	01/2018	03/2020	1871.34	26
364	SONAPUR TO GUWAHTI (AS-3)	NHAI	12/2003	03/2008	08/2020	245	149
365	NALBARI T BIJNI (AS-7)	NHAI	12/2003	04/2008	03/2020	208	143
366	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	NHAI	06/2011	06/2013	08/2020	600	86
367	HARIDWAR DEHRADUN APPROVED LENGTH 69	NHAI	11/2011	10/2013	08/2020	478.51	82
368	2 LANING WITH PS OF GULABPURA - UNIARA	NHAI	10/2015	10/2017	03/2020	597	29

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
369	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D	NHAI	09/2015	05/2018	05/2020	414.51	24
370	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	09/2020	531.13	28
371	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	NHAI	10/2015	05/2018	06/2020	593.26	25
372	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	NHAI	12/2015	03/2019	04/2021	649.5	25
373	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3	NHAI	08/2015	05/2018	09/2020	505	28
374	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A	NHAI	12/2015	06/2019	12/2020	2168.66	18
375	FOUR LANING OF PARWANOO -SOLAN	NHAI	09/2015	03/2018	03/2020	934.46	24
376	FOUR LANING OF YADGIRI - WARANGAL	NHAI	12/2015	11/2018	06/2020	1423.96	19
377	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A	NHAI	12/2015	12/2018	07/2020	2136.97	19
378	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II)	NHAI	01/2016	06/2018	06/2020	815.28	24
379	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I)	NHAI	01/2016	06/2018	06/2020	1027.53	24
380	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III)	NHAI	06/2016	07/2018	04/2020	667	21
381	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II)	NHAI	12/2015	06/2018	04/2020	667	22
382	FOUR LANING OF FORBESGANJ - JOGBANI	NHAI	08/2015	04/2018	12/2020	322.09	32
383	FOUR LANING OF CHANDIGARH - KHARAR	NHAI	10/2015	12/2017	06/2020	447.29	30
384	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1)	NHAI	12/2015	04/2018	03/2020	726.67	23
385	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	NHAI	03/2016	03/2019	11/2020	701.4	20
386	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA	NHAI	03/2016	11/2018	08/2020	229.37	21
387	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL	NHAI	03/2016	03/2019	11/2020	870	20
388	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH	NHAI	02/2016	08/2018	03/2020	707.82	19
389	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791	NHAI	03/2016	04/2019	07/2020	899	15
390	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K	NHAI	02/2016	07/2018	05/2020	641.17	22
391	NAGPUR RING ROAD PACKAGE-1	NHAI	03/2016	07/2019	12/2020	546	17

DOA -> Date of Approval

DOC -> Date of Commissioning

499

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
392	NAGPUR RING ROAD PACKAGE-2	NHAI	03/2016	07/2019	12/2020	591.66	17
393	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T	NHAI	04/2016	06/2018	03/2020	804.97	21
394	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	NHAI	08/2016	09/2019	03/2020	1388.34	6
395	FOUR LANING OF BARHI-HAZARIBAGH NH-33	NHAI	08/2016	08/2018	01/2020	323.72	17
396	HOSPET-BELLARY-KARNATAKA AP BORDER	NHAI	08/2016	03/2019	08/2020	1167.42	17
397	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73	NHAI	08/2016	05/2019	03/2020	248.97	10
398	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S	NHAI	09/2016	08/2019	03/2021	2510.04	19
399	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	NHAI	09/2016	08/2019	12/2020	950.69	16
400	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI	NHAI	11/2016	03/2019	02/2021	400.25	23
401	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT	NHAI	11/2016	03/2019	03/2021	446.17	24
402	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	NHAI	11/2012	07/2018	02/2020	605.84	19
403	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2	NHAI	03/2017	03/2020	11/2020	1373.28	8
404	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580)	NHAI	03/2017	03/2017	11/2020	1059.73	44
405	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN	NHAI	03/2017	03/2020	08/2021	754.54	17
406	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE	NHAI	03/2017	03/2020	05/2021	235.48	14
407	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	03/2021	1288.07	12
408	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	NHIDCL	12/2016	01/2017	01/2020	138.93	36
409	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	NHIDCL	01/2017	03/2017	03/2022	1253.1	60
410	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	NHIDCL	03/2017	04/2017	03/2021	284.09	47
411	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS	NHIDCL	02/2017	04/2017	02/2021	168.32	46
412	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	NHIDCL	02/2017	04/2017	02/2021	180.57	46
413	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS	NHIDCL	02/2017	04/2017	02/2021	216.71	46
414	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	NHIDCL	02/2017	04/2017	02/2021	167.28	46

DOA -> Date of Approval

DOC -> Date of Commissioning

500

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
415	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	NHIDCL	03/2016	08/2016	03/2020	373.07	43
416	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	NHIDCL	03/2016	08/2016	06/2020	396.52	46
417	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	NHIDCL	03/2016	08/2016	03/2020	429.52	43
418	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	NHIDCL	02/2017	09/2018	08/2020	387	23
419	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS	MoRTH	02/2018	03/2018	04/2020	279.44	25
420	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175	MoRTH	09/2016	01/2019	03/2020	287.34	14
421	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A	MoRTH	01/2017	09/2019	09/2020	373.82	12
422	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS	MoRTH	01/2016	07/2018	09/2020	809.16	26
423	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM	MoRTH	03/2016	06/2019	07/2020	877.79	13
424	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS	MoRTH	01/2017	03/2019	06/2020	247.25	15
425	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200	MoRTH	10/2017	10/2019	12/2020	1069.59	14
426	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000	MoRTH	03/2018	11/2020	05/2021	170.57	6
427	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12	MoRTH	10/2015	12/2015	01/2020	333.21	49
428	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	NHIDCL	08/2017	10/2018	10/2021	517.57	36
429	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS	MoRTH	03/2018	03/2018	05/2020	162.56	26
430	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS	MoRTH	03/2018	08/2018	06/2020	166.21	22
431	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA	MoRTH	02/2018	03/2018	07/2020	169.63	28
432	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID	MoRTH	11/2017	02/2018	05/2020	235.91	27
433	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS	MoRTH	11/2017	02/2018	05/2020	184.62	27
434	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP	MoRTH	03/2018	11/2019	05/2020	191.21	6
435	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND	MoRTH	03/2016	08/2019	08/2021	160.27	24
436	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N	MoRTH	06/2016	08/2019	08/2021	236.78	24
437	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH.	MoRTH	01/2017	03/2017	09/2020	205.05	42

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
438	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS	MoRTH	03/2018	03/2018	12/2020	214.69	33
439	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS	MoRTH	03/2018	08/2018	06/2020	217.22	22
440	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS	MoRTH	03/2018	03/2018	04/2020	233.04	25
441	2L+PS OF THIKRI ANJAD SECTION OF NH-347B	MoRTH	11/2017	07/2018	06/2020	249.05	23
442	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS	MoRTH	11/2017	02/2018	09/2020	254.17	31
443	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO	MoRTH	11/2016	01/2018	01/2020	378.24	24
444	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69	MoRTH	11/2016	05/2017	03/2020	290.15	34
445	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD	MoRTH	01/2017	08/2017	03/2020	319.28	31
446	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V	MoRTH	02/2017	11/2017	03/2020	429.43	28
447	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3	MoRTH	03/2018	08/2018	03/2020	228.32	19
448	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU	MoRTH	03/2018	08/2018	02/2020	244.95	18
449	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG	MoRTH	03/2018	08/2018	02/2020	289.67	18
450	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (	MoRTH	03/2018	07/2018	01/2020	297.12	18
451	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON	MoRTH	10/2016	02/2019	06/2020	298.32	16
452	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ	MoRTH	10/2016	03/2019	03/2020	248.83	12
453	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION	MoRTH	01/2017	05/2019	03/2020	300	10
454	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC	MoRTH	05/2014	08/2016	12/2020	199.98	52
455	DIGRAS DARWAH KARANJA	MoRTH	01/2017	06/2019	06/2020	391.06	12
456	WADI TO ASOLA	MoRTH	01/2017	09/2019	09/2020	363.82	12
457	MANGAON TO DIGHI PORT	MoRTH	01/2017	07/2019	07/2020	457.52	12
458	WAKAN PALI KHOPOLI	MoRTH	01/2017	05/2019	05/2020	376.19	12
459	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO	MoRTH	07/2016	10/2019	06/2020	208.88	8
460	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION	MoRTH	02/2017	05/2019	05/2021	157.32	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
461	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT	MoRTH	05/2018	05/2018	05/2020	171.6	24
462	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730	MoRTH	03/2016	05/2019	03/2020	249.5	10
463	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM.	MoRTH	11/2017	03/2018	09/2020	392.33	30
464	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MoRTH	08/2010	09/2014	06/2020	186.96	69

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
465	CENTRAL DISPATCH YARD	RINL	08/2015	08/2018	02/2020	320.66	18
466	INSTALLATION OF NEW HOT STRIP MILL AT RSP	SAIL	04/2015	04/2018	01/2020	3127.3	21
467	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	07/2020	15525	62
468	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	SAIL	11/2016	06/2019	11/2020	262.87	17
469	FORGED WHEEL PLANT	RINL	04/2014	09/2018	02/2020	1682.85	17
470	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	SAIL	05/2015	12/2017	03/2020	1154.18	27
471	NEW SINTER PLANT AT BOKARO STEEL PLANT	SAIL	03/2015	10/2017	06/2020	1034.01	32
472	COKE OVEN BATTERY-5	RINL	12/2011	12/2017	03/2020	2858	27

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
473	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	05/2020	13334	58
474	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	BSNL	01/2018	10/2018	02/2020	231.8	16

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
475	AHMEDABAD METRO RAIL PROJECT PHASE 1	MEGA	11/2014	12/2018	07/2020	10773	19
476	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	CPWD	08/2016	04/2019	05/2020	294	13
477	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	CPWD	02/2014	03/2015	10/2020	216.69	67
478	NSG AT KOLKATA	CPWD	10/2014	04/2018	06/2020	162.88	26

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
479	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	CPWD	09/2012	03/2016	09/2020	171.86	54
480	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	03/2021	1219.21	17
481	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	CPWD	01/2010	10/2012	03/2020	165.23	89
482	REDEVELOPMENT OF EAST KIDWAI NAGAR	NBCC	06/2012	11/2019	05/2020	4264	6
483	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	03/2020	5181.79	32
484	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	01/2015	05/2020	23136	64
485	CHENNAI METRO RAIL LTD (PHASE 1 EXT)	CMRL	06/2016	03/2018	06/2020	3770	27
486	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD	CPWD	10/2016	03/2020	05/2021	209.84	14
487	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	CPWD	02/2016	06/2017	03/2021	496.18	45
488	BANGALORE METRO RAIL PROJECT PHASE-2	BMRCL	02/2014	02/2019	03/2020	26405.14	13
489	IRRIGATION WORK OF BAGMATI	HSCL	10/2005	03/2015	03/2021	956	72
490	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	CPWD	06/2015	04/2019	12/2020	197.33	20
491	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	CPWD	02/2014	05/2017	03/2020	388	34
492	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	CPWD	12/2015	10/2019	07/2020	209	9
493	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	CPWD	02/2014	08/2016	01/2020	156.57	41
494	RESIDENTIAL QUATERS FOR HAL, BANGLORE	CPWD	12/2016	02/2020	09/2020	246.31	7
495	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	CPWD	01/2018	05/2020	02/2021	430	9
496	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	CPWD	10/2017	11/2019	08/2020	271.9	9
497	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	CPWD	10/2016	04/2018	08/2020	248.2	28
498	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST)	CPWD	09/2017	03/2020	03/2021	150.29	12
499	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	CPWD	12/2016	07/2019	08/2020	549.31	13

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
500	SEWAGE TREATMENT PLANT AT JAGJEETPUR	UKJaInigam	03/2017	08/2019	02/2020	273.37	6

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	AND SARAI						
501	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	12/2021	10151.04	21

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JANUARY 2020)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	6840	3348
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	11459	16580	5121
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12320	17079	4759

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	314.61	441.33	126.72

COAL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
5	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	152.43	459.49	307.06
6	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	162.76	349.28	186.52
7	RANIGANJ MASTER PLAN	ECL	08/2009	08/2019	2661.73	5146.48	2484.75
8	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	5907.11	7080.41	1173.3
9	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	249.03	448.86	199.83
10	BHANEGAON OC	WCL	02/2015	03/2023	187.94	409.68	221.74

COMMERCE AND INDUSTRY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
11	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	IICC	11/2017	12/2019	4773	5178	405

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
12	AIIMS BILASPUR	NBCC	04/2018	09/2021	1351	1471	120
13	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR	CPWD	03/2019	09/2025	1577	1828	251

HUMAN RESOURCE DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
14	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	MITES	09/2013	09/2014	484.32	626.26	141.94

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JANUARY 2020)

PETROLEUM							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
15	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	993	1693	700
16	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	607.06	714.25	107.19
17	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)	ONGC	02/2017	05/2021	4006.83	4475.92	469.09
18	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	2915	4915	2000
19	MUMBAI REFINERY EXPANSION PROJECT	HPCL	09/2015	03/2020	4199	5060	861
20	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	4497	6025	1528
21	VISAKH REFINERY MODERNISATION PROJECT	HPCL	07/2016	07/2020	20928	26264	5336
22	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	4588.29	5245.96	657.67
23	HALDIA LPG IMPORT FACILITY	BPCL	03/2015	10/2018	694	1097.54	403.54
24	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	871.35	1200	328.65
25	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	2059.63	2665.65	606.02
26	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	OIL	01/2018	02/2020	543.91	682.9	138.99
27	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	1112	1507.24	395.24
28	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	861.79	1683.06	821.27
29	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	IOCL	01/2015	12/2020	1823	3027.9	1204.9
30	PARADIP HYDERABAD PIPELINE	IOCL	01/2015	12/2020	2321	3338	1017
POWER							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
31	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	9997.11	6077.52
32	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	01/2018	11638.55	12865.92	1227.37
33	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	11130.19	14719.1	3588.91
34	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	19496.34	13211.01
35	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	4824.12	5071.94	247.82
36	NORTH EASTERN REGION POWER SYSTEM	PGCIL	12/2014	12/2018	5111.33	6880.36	1769.03

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
	IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES						
37	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	4754.42	9072.36	4317.94
38	PAKRI BARWADIH COAL MINING PROJECT	NTPC	10/2004	10/2017	4237.96	4552	314.04
39	KHARGONE STPP STAGE I (1320 MW)	NTPC	03/2015	01/2020	9870.51	11148.86	1278.35
40	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	NTPC	07/2012	08/2017	1527	1801.07	274.07
41	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	10/2017	11846	12739.82	893.82
42	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	2491.58	4397.8	1906.22
43	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	02/2017	9750.89	12176.28	2425.39
44	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	12964.6	17304	4339.4
45	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	07/2012	5353	9583	4230
46	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	1381.84	1592.34	210.5
47	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	14366.58	15164.05	797.47
48	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	12/2018	12532.44	13740.53	1208.09
49	TANDA TPP STAGE-II (2X660 MW)	NTPC	09/2014	07/2019	9188.98	10016.1	827.12
50	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	5867.38	2888.9
51	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	8692.97	21312.11	12619.14
52	SYTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	487.49	639.46	151.97
53	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	2496.9	7927.34	5430.44
54	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	1364.52	1891.41	526.89

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
55	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR	NFR	04/1983	03/2019	297.32	614	316.68
56	KODERMA-RANCHI VIA BARKAKANA (NL), ECR	ECR	03/1999	N.A.	1033.07	3376	2342.93
57	KOTLIPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	1045.2	2120.16	1074.96

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
58	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	M RTP	03/2000	12/2006	1049.69	3404.92	2355.23
59	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	1188.91	1619.48	430.57
60	RAMGANJ MUNDI-BHOPAL (NL), WCR	WCR	04/2001	03/2021	424.6	2909.99	2485.39
61	CHHINDWARA - NAGPUR (GC)(SECR)	SECR	04/2005	N.A.	383.79	1413.76	1029.97
62	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	477.88	751.55	273.67
63	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	ECR	04/2003	N.A.	528.65	2066.78	1538.13
64	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	2393.47	5021.45	2627.98
65	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	171.1	275.08	103.98
66	TIDIVANAM-NAGARI (NL)	SR	09/2006	N.A.	582.83	2300	1717.17
67	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	SR	09/2006	N.A.	227.4	900	672.6
68	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII' -AGASTIYAMPALLI	SR	09/2007	02/2019	724.69	2072.5	1347.81
69	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	810.78	1928.07	1117.29
70	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	133.41	396	262.59
71	NADIKUDE-SRI KALAHASTI	SCR	04/2011	03/2021	2288.7	2643.25	354.55
72	SRINIVASA-PURA-MADANAPALLI NL	SWR	04/2013	N.A.	296	466.65	170.65
73	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	SWR	04/2013	N.A.	558	692.43	134.43
74	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL	NR	04/2007	N.A.	336.91	791.39	454.48
75	BHANUPALI-BILASPUR BERI NL	RVNL	04/2008	12/2026	2966.99	7000	4033.01
76	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	287	750	463
77	BHADRACHALAM-KOVVUR	SCR	04/2012	N.A.	923.23	2184.83	1261.6
78	MANUGURU-RAMAGUNDAM	SCR	04/2013	N.A.	1112	2911.84	1799.84
79	3RD LINE BETWEEN BHUSAWAL-JALGAON	CR	04/2011	03/2019	184.06	312	127.94
80	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	4084.69	2745.21

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
81	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	2326.52	5806.81	3480.29
82	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	532.87	2145	1612.13
83	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	385.2	1532	1146.8
84	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	MRTPT	04/2006	06/2013	495.74	734.01	238.27
85	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	4454.17	12524	8069.83
86	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	2923.13	3791.66	868.53
87	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	NFR	04/2000	12/2008	1180.19	4541	3360.81
88	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	614.45	451.58
89	AHMEDABAD-BOTAD (GC)	RVNL	04/2012	12/2021	975.62	1082.32	106.7
90	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	12/2019	246.08	348.55	102.47
91	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	MRTPT	03/2013	03/2016	4874.58	8574.97	3700.39
92	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	295	477.31	182.31
93	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP	NER	03/2007	12/2021	243.78	895	651.22
94	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP	NER	03/2013	N.A.	307	1409.09	1102.09
95	ANGAMALI-SABARIMALA (N.L.)(SR)	SR	10/1998	N.A.	1566	2815.62	1249.62
96	KODERMA-TILAIYA (NL), ECR	ECR	04/2002	N.A.	459.91	1625.87	1165.96
97	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	1614.59	1870.41	255.82
98	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE	NER	04/2017	01/2018	1343	1476.15	133.15
99	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	SR	02/2015	03/2020	760	1182.31	422.31
100	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	SR	02/1996	03/2005	268.87	950	681.13
101	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	585.93	1268.32	682.39
102	MANMAD-PARBHANI-NANDED-SECUNDERABAD- GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	SCR	04/2017	03/2022	119.73	449.39	329.66

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
103	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	1908.51	2686.63	778.12
104	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	582.13	1247.64	665.51
105	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	942.95	1120	177.05
106	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	948.04	1500	551.96
107	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	713.48	2300	1586.52
108	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	927.01	1200	272.99
109	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	1027.4	2373	1345.6
110	BONDAMUNDA RANCHI DOUBLING	SER	03/2016	03/2021	1724.2	1993.24	269.04
111	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	969.83	1312.96	343.13
112	DIGARU-HOJAI (102 KM)	NFR	04/2015	03/2021	870.96	2136.01	1265.05
113	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	701.61	810.02	108.41
114	KOTTAVALSA - KORAPUT DOUBLING	ECOR	04/2015	03/2022	2499.71	3382.95	883.24
115	MUZAFFARPUR-SITAMARHI NEW LINE	ECR	01/1991	07/2014	332.15	546.71	214.56
116	VIJAYAWADA-GUDUR	RVNL	04/2015	12/2023	3246.26	3548.67	302.41
117	DAUND - MANMAD (236 KM)	CR	02/2016	03/2023	1876	2081.27	205.27
118	VAIBHAVWADI -KOLHAPUR (107 KM)	CR	02/2016	03/2024	2750	3438.51	688.51
119	PUNE-NASIK (265 KM)	CR	02/2016	03/2024	2425	5341.68	2916.68
120	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	DFCC	10/2006	N.A.	11589	28181	16592
121	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	ER	04/2005	03/2017	595.51	769.4	173.89
122	PIRPAINTI-BHAGALPUR	ER	04/2011	N.A.	261.38	492.84	231.46
123	BANDEL-BOINCHI 3RD LINE	ER	04/2011	N.A.	288.35	402.48	114.13
124	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	915.98	2137.81	1221.83
125	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR	ER	04/2007	N.A.	450	1261.34	811.34

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
126	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	ER	04/1987	03/2006	406.99	545.7	138.71
127	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI	SR	04/2011	03/2019	120.7	1800	1679.3
128	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	632.68	816.55	183.87
129	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	03/2019	314	728	414
130	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	NFR	04/1999	N.A.	819.23	1871	1051.77
131	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	03/2020	414.84	661	246.16
132	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	373.87	132.35
133	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	03/2020	242.22	471	228.78
134	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	03/2021	906.46	6000.6	5094.14
135	MADURAI-BODINAYAKKANUR	SR	04/2008	N.A.	164.41	450	285.59
136	ERODE-PALANI	SR	04/2008	N.A.	288.57	1140	851.43
137	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	569.63	670	100.37
138	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	NFR	04/2010	N.A.	221.42	380	158.58
139	KURUPPANTHARA-CHINGAVANAM	SR	04/2007	N.A.	270.14	457.08	186.94
140	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	SR	04/1999	N.A.	198.68	556.64	357.96
141	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	SR	04/2013	N.A.	839	1500	661
142	CHENNAI-CUDDALORE VIA MAMALLAPURAM	SR	04/2008	N.A.	523.52	2300	1776.48
143	ATTIPPATTU PUTTUR	SR	04/2008	02/2019	151.84	1105	953.16
144	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	NFR	04/2013	03/2019	1798	2496.67	698.67
145	HAJIPUR-RAMDAYALUNAGAR DOUBLING	ECR	04/2013	N.A.	213.01	440	226.99
146	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	548	819.01	271.01
147	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	ECR	04/2004	N.A.	372.14	1470.5	1098.36
148	MOTIHARI-SITAMARHI (NL)	ECR	04/2006	N.A.	211	1006	795

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
149	CHHAPRA-MUZAFFARPUR (NL)	ECR	04/2006	N.A.	378.56	1858.75	1480.19
150	SAKRI-HASANPUR ROAD (NL)	ECR	04/1999	N.A.	325	735.2	410.2
151	BIHTA-AURANGABAD (NL)	ECR	04/2008	N.A.	326.2	2995.01	2668.81
152	GAYA-CHATRA (NL)	ECR	04/2008	N.A.	415.67	549.75	134.08
153	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	12/2018	258.2	358.68	100.48
154	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	651	1009	358
155	BOWAICHANDI-ARAMBAGH	SER	04/2010	N.A.	267.37	620	352.63
156	ALWAR-BANDIKUI DOUBLING	NWR	04/2013	02/2019	242.09	410	167.91
157	PUSHKAR-MERTA	NWR	04/2013	N.A.	323	432.22	109.22
158	AJMER-KOTA (NASIRABAD-JAUNDRI)	NWR	04/2013	N.A.	822	1099.54	277.54
159	THIYAT HAMIRA-SANU	NWR	04/2013	10/2018	236.93	350.45	113.52
160	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	2912.96	3845.6	932.64
161	RATLAM-DUNGARPUR VIA BANSWARA (NL)	NWR	04/2011	N.A.	2082.75	4262.36	2179.61
162	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	320.66	858.96	538.3
163	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	NWR	05/2015	N.A.	873.71	1980.21	1106.5
164	SAMASTIPUR-DARBANGHA	ECR	05/2015	N.A.	380	519.33	139.33
165	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	SER	04/2012	12/2016	148.77	377	228.23
166	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	1111.99	1539.28	427.29
167	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	1503.71	2200	696.29
168	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	829.74	1310.23	480.49
169	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	09/1995	03/2020	303.98	980	676.02
170	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	393.46	1026	632.54
171	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN	NFR	02/1999	04/2010	380.6	1871	1490.4

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
172	JALANDHAR-PATHANKOT-JAMMU TAWI	NR	03/2002	03/2016	625	859	234
173	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	2288	4970.11	2682.11
174	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	WR	02/1991	03/2019	551.51	809.07	257.56
175	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	644.78	890	245.22
176	CHAMPA-JHARSUGUDA 3RD LINE	SECR	04/2008	12/2019	872	1226.51	354.51
177	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	229	852.5	623.5
178	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	ECR	04/1991	N.A.	329.39	1483.14	1153.75
179	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR	ECR	04/1998	N.A.	180.82	726.31	545.49
180	MUZAFFARPUR SAGauli DOUBLING 100.60 KM	ECR	04/2016	03/2021	731.64	1185.73	454.09
181	SAGauli VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	744.04	1215.54	471.5
182	BURHWAL - GONDA - 3RD RUNNING LINE.	NER	04/2016	N.A.	602.5	714.34	111.84
183	CHANDIGARH-BADDI	NR	04/2007	03/2023	328.14	1540	1211.86
184	WESTERN DEDICATED FREIGHT CORRIDOR	DFCC	11/2007	03/2020	16592	51101	34509
185	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	04/2020	511.86	1756	1244.14
186	MUNEERABAD-MAHABOBNAGAR(NL), SCR	SCR	04/1997	03/2000	1723	3472.59	1749.59
187	NANDYAL-YERRAGUNTLA(NL), SCR	SCR	03/1996	02/2009	164.36	1050	885.64
188	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	2298.42	2733.86	435.44
189	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	3951.98	4724.3	772.32
190	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	2500	27949	25449
191	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	450	2200	1750
192	DAUSA-GANGAPUR CITY(NL), NWR	NWR	02/1997	02/2019	410.08	886.41	476.33
193	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	324.73	1050	725.27
194	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	8248.5	8000.84

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
195	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	495.44	2980.41	2484.97
196	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	2271.5	4517.49	2245.99
197	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	RVNL	04/2010	03/2023	2127	2900	773
198	QADIAN-BEAS	NR	04/2011	N.A.	205.22	841.9	636.68
199	HARIDWAR-LAKSAR	NR	04/2012	N.A.	219.83	346.63	126.8
200	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	03/2020	704.31	927.94	223.63
201	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	02/2012	499.96	680.68	180.72
202	HANSDIHA-GODDA NL	ER	04/2011	03/2020	542.18	693.8	151.62
203	TARAKESHWAR-MAGRA NEW BG LINE	ER	04/2010	N.A.	365.17	527.54	162.37
204	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	792.89	1377.48	584.59
205	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	3503.69	3975.22	471.53
206	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	2913.51	4639	1725.49
207	ETAWAH-MAINPURI (NL),NCR	NCR	04/1997	12/2008	120	346	226
208	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	607.09	1425.44	818.35
209	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	12/2017	1185.64	1844.47	658.83

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
210	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	NHAI	12/2003	02/2009	280	520	240
211	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	1108	2967.5	1859.5
212	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	196	655.17	459.17
213	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	199.81	340.14	140.33
214	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	MORTH	12/2011	02/2012	156.63	276	119.37
215	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	MORTH	03/2012	05/2012	207.03	389.45	182.42
216	BRAHMPUTRA BRIDGE,NH NO-31	NHAI	12/2003	04/2010	217.61	360.84	143.23

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
217	DEVELOPMENT AND OPERATION OF BIKANER-SURATGARH SECTION OF NH-15 BY 2L+PS IN THE STATE OF RAJASTHAN	MORTH	03/2009	09/2013	501	671.54	170.54
218	NAGPUR-BIKANER OF NH-11 (2L+PS) UNDER PPP.	MORTH	01/2012	01/2014	378.07	478.73	100.66
219	REHABILITATION AND UPGRADE OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7	MORTH	04/2014	08/2017	279.7	398.52	118.82
220	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A 0	MORTH	08/2014	11/2017	823.2	937.76	114.56
221	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 0	MORTH	08/2014	11/2017	600.87	720.97	120.1
222	FOUR LANE OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4	NHAI	03/2018	N.A.	642.13	807	164.87
223	SIX LANE AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA	NHAI	03/2018	N.A.	634.7	931.21	296.51
224	FOUR LANE OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N	NHAI	03/2018	N.A.	2065.96	2169	103.04
225	6-LANE OF KOZHICKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH	NHAI	02/2018	N.A.	1424.77	1853.42	428.65
226	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1	MORTH	12/2010	01/2019	169.26	299	129.74
227	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MORTH	08/2010	09/2014	186.96	305.61	118.65
228	REHABILITATION AND UPGRADE OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH	MORTH	10/2013	03/2017	445.89	653.29	207.4
229	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	1124.11	1232.76	108.65
230	SIX LANE OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(0	NHAI	03/2017	03/2020	993.16	1434	440.84
231	SIX LANE OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	NHAI	03/2017	03/2020	831.58	1177	345.42
232	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	NHAI	03/2017	03/2020	2064.99	2447	382.01
233	REHABILITATION AND UPGRADE BY 4-LANE OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	1288.07	1420	131.93
234	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	NHAI	03/2017	03/2020	1041.62	1187.1	145.48
235	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	NHAI	03/2017	03/2020	744.64	982	237.36
236	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	NHAI	03/2017	03/2020	1184.71	1310	125.29
237	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF	NHAI	03/2018	N.A.	1029.96	1261.05	231.09
238	FOUR LANE OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)	NHAI	03/2018	03/2021	1532.62	2499	966.38

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
239	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF	NHAI	02/2018	N.A.	1052.21	1449	396.79
240	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C	NHAI	03/2018	N.A.	1120.57	1332	211.43
241	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR.	NHAI	03/2018	N.A.	925.4	1197	271.6
242	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA	NHAI	02/2018	N.A.	2177.8	2450	272.2
243	SIX-LANING OF BANGALORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT	NHAI	02/2018	N.A.	1995.34	2400	404.66
244	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	NHAI	11/2012	07/2018	605.84	722.46	116.62
245	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	NHAI	09/2016	08/2019	950.69	1108	157.31
246	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	NHAI	08/2016	09/2019	1388.34	2587.5	1199.16
247	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	NHAI	03/2016	04/2019	1587.49	2982	1394.51
248	MEERUT-BULANDSHAHR	NHAI	01/2016	N.A.	683.24	987.94	304.7
249	FOUR LANING OF CHANDIGARH - KHARAR	NHAI	10/2015	12/2017	447.29	746.43	299.14
250	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	11/2015	1055	1601.77	546.77
251	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2	NHAI	11/2015	05/2018	867.66	1464.24	596.58
252	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	531.13	727	195.87
253	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	MORTH	08/2010	10/2010	195.04	377.99	182.95
254	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	MORTH	11/2011	09/2015	954.43	1191.51	237.08
255	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	MORTH	11/2010	02/2011	470.2	630.36	160.16
256	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	MORTH	11/2013	05/2017	497.05	881.05	384
257	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270	MORTH	10/2013	03/2017	445.89	653.29	207.4
258	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I	NHAI	08/2015	02/2018	723.54	1286.84	563.3
259	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	1928.22	2945	1016.78
260	NASHRI- CHANANI	NHAI	05/2011	06/2015	2159	2519	360
261	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	1266.6	1544	277.4

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN RS. 100 CRORE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
262	INDORE-DEWAS(NH-3)	NHAI	11/2010	05/2013	325	475	150
263	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MORTH	08/2010	10/2010	193.69	327.92	134.23
264	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	MORTH	11/2010	03/2011	624.41	992.67	368.26
265	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	NHAI	12/2003	11/2008	167.64	435.78	268.14
266	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	155.04	255.23	100.19
SHIPPING AND PORTS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
267	JAL MARG VIKAS PROJECT	IWAI	01/2018	03/2023	4200	5369.18	1169.18
STEEL							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
268	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	15525	23140	7615
TELECOMMUNICATIONS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
269	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	13334	24664	11330
URBAN DEVELOPMENT							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
270	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCL	05/2005	02/2014	768.88	1113.34	344.46
271	REDEVELOPMENT OF EAST KIDWAI NAGAR	NBCC	06/2012	11/2019	4264	4720.73	456.73
272	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	5181.79	6218.14	1036.35
273	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	114.26	266	151.74
274	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	14600	19058	4458
275	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	1219.21	2000	780.79
276	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	CPWD	02/2014	05/2017	388	490	102

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JANUARY 2020)

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
277	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	10151.04	55548.87	45397.83

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JANUARY 2020)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	03/2023	1,2320.00	1,7079.00	4759	75
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	09/2021	1,1459.00	1,6580.00	5121	69
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2021	3492.00	6840.00	3348	133

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2020	314.61	441.33	126.72	21

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
5	RANIGANJ MASTER PLAN	ECL	08/2009	08/2019	08/2024	2661.73	5146.48	2484.75	60
6	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2021	162.76	349.28	186.52	72
7	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2024	249.03	448.86	199.83	144
8	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	03/2020	5907.11	7080.41	1173.3	51
9	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	459.49	307.06	60

COMMERCE AND INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
10	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	IICC	11/2017	12/2019	09/2020	4773.00	5178.00	405	9

HUMAN RESOURCE DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
11	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	RITES	09/2013	09/2014	12/2020	484.32	626.26	141.94	75

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

520

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JANUARY 2020)

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
12	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	02/2022	1112.00	1507.24	395.24	32
13	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)	ONGC	02/2017	05/2021	12/2021	4006.83	4475.92	469.09	7
14	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	02/2021	4497.00	6025.00	1528	26
15	VISAKH REFINERY MODERNISATION PROJECT	HPCL	07/2016	07/2020	07/2022	2,0928.00	2,6264.00	5336	24
16	HALDIA LPG IMPORT FACILITY	BPCL	03/2015	10/2018	02/2020	694.00	1097.54	403.54	16
17	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	03/2020	2059.63	2665.65	606.02	60
18	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	02/2022	2915.00	4915.00	2000	110
19	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	02/2020	861.79	1683.06	821.27	81
20	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	02/2020	4588.29	5245.96	657.67	18

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
21	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	12/2020	5111.33	6880.36	1769.03	24
22	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	10/2017	03/2020	1,1846.00	1,2739.82	893.82	29
23	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	12/2020	4754.42	9072.36	4317.94	24
24	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	06/2020	2496.90	7927.34	5430.44	126
25	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	07/2012	09/2020	5353.00	9583.00	4230	98
26	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	03/2022	1,4366.58	1,5164.05	797.47	33
27	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	06/2021	1,2964.60	1,7304.00	4339.4	37

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

521

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
28	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	02/2017	06/2020	9750.89	1,2176.28	2425.39	40
29	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2021	3919.59	9997.11	6077.52	147
30	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	08/2023	6285.33	1,9496.34	13211.0	155
31	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	03/2020	4824.12	5071.94	247.82	89
32	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	01/2018	03/2020	1,1638.55	1,2865.92	1227.37	26
33	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	03/2022	1,1130.19	1,4719.10	3588.91	103
34	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	02/2020	1364.52	1891.41	526.89	46
35	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2021	2978.48	5867.38	2888.9	105
36	TANDA TPP STAGE-II (2X660 MW)	NTPC	09/2014	07/2019	09/2020	9188.98	1,0016.10	827.12	14
37	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	12/2018	08/2020	1,2532.44	1,3740.53	1208.09	20
38	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	11/2022	1381.84	1592.34	210.5	38
39	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2022	2491.58	4397.80	1906.22	114
40	SYTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	02/2020	487.49	639.46	151.97	68
41	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	08/2021	8692.97	2,1312.11	12619.1	118

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
42	JALANDHAR-PATHANKOT-JAMMU TAWI	NR	03/2002	03/2016	03/2021	625.00	859.00	234	60
43	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	WR	02/1991	03/2019	03/2020	551.51	809.07	257.56	12

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

522

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
44	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	03/2023	229.00	852.50	623.5	15
45	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	12/2020	585.93	1268.32	682.39	22
46	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	03/2020	927.01	1200.00	272.99	12
47	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	03/2021	713.48	2300.00	1586.52	12
48	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	03/2021	948.04	1500.00	551.96	12
49	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	06/2022	942.95	1120.00	177.05	39
50	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	09/2022	582.13	1247.64	665.51	6
51	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE-GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	SCR	04/2017	03/2022	12/2022	119.73	449.39	329.66	9
52	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	SR	02/2015	03/2020	06/2021	760.00	1182.31	422.31	15
53	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	03/2022	744.04	1215.54	471.5	12
54	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM	ECR	04/2016	03/2021	03/2022	731.64	1185.73	454.09	12
55	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	03/2020	385.20	1532.00	1146.8	12
56	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	03/2020	532.87	2145.00	1612.13	12
57	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	10/2021	2326.52	5806.81	3480.29	79
58	DAUSA-GANGAPUR CITY(NL),NWR	NWR	02/1997	02/2019	06/2021	410.08	886.41	476.33	28
59	NANGALDAM-TALWARA(NL),NR	NR	03/1981	07/2012	03/2024	450.00	2200.00	1750	140
60	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	NR	03/1995	11/2002	06/2022	2500.00	2,7949.00	25449	235
61	NEW WORK FOR CONSTRUCTION OF	RVNL	04/2010	03/2016	03/2025	3951.98	4724.30	772.32	108

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

523

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)								
62	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	2733.86	435.44	141
63	MUNEERABAD-MAHABOBNAGAR(NL), SCR	SCR	04/1997	03/2000	03/2021	1723.00	3472.59	1749.59	252
64	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	03/2020	477.88	751.55	273.67	96
65	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	03/2025	2913.51	4639.00	1725.49	108
66	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	03/2023	3503.69	3975.22	471.53	12
67	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	03/2022	792.89	1377.48	584.59	12
68	HANSDIHA-GODDA NL	ER	04/2011	03/2020	03/2021	542.18	693.80	151.62	12
69	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	02/2012	03/2025	499.96	680.68	180.72	157
70	3RD LINE BETWEEN BHUSAWAL - JALGAON	CR	04/2011	03/2019	03/2020	184.06	312.00	127.94	12
71	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	03/2021	287.00	750.00	463	111
72	NADIKUDE-SRI KALAHASTI	SCR	04/2011	03/2021	03/2024	2288.70	2643.25	354.55	36
73	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR	NFR	04/1983	03/2019	03/2020	297.32	614.00	316.68	12
74	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2023	1045.20	2120.16	1074.96	168
75	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	03/2025	1188.91	1619.48	430.57	72
76	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	03/2024	607.09	1425.44	818.35	133
77	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	12/2017	03/2020	1185.64	1844.47	658.83	27
78	RAMGANJMUNDI-BHOPAL (NL), WCR	WCR	04/2001	03/2021	03/2023	424.60	2909.99	2485.39	24

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

524

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
79	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	06/2020	133.41	396.00	262.59	135
80	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	06/2024	810.78	1928.07	1117.29	36
81	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	SR	09/2007	02/2019	02/2020	724.69	2072.50	1347.81	12
82	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	03/2022	2393.47	5021.45	2627.98	96
83	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	RVNL	04/2010	03/2023	03/2024	2127.00	2900.00	773	12
84	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	03/2022	2271.50	4517.49	2245.99	12
85	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	03/2021	495.44	2980.41	2484.97	204
86	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2023	247.66	8248.50	8000.84	178
87	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	03/2020	324.73	1050.00	725.27	96
88	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	03/2021	1180.19	4541.00	3360.81	147
89	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	06/2024	2923.13	3791.66	868.53	183
90	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2022	4454.17	1,2524.00	8069.83	132
91	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	04/2020	01/2021	511.86	1756.00	1244.14	9
92	TIRUCHIRAPPALI-NAGORE-KARAIKKAL (SR) (GC)	SR	09/1995	03/2020	03/2021	303.98	980.00	676.02	12
93	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	03/2021	829.74	1310.23	480.49	12
94	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	03/2022	1503.71	2200.00	696.29	24
95	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	03/2022	1111.99	1539.28	427.29	37

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

525

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
96	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	SER	04/2012	12/2016	03/2020	148.77	377.00	228.23	39
97	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	03/2021	1614.59	1870.41	255.82	24
98	ALWAR-BANDIKUI DOUBLING	NWR	04/2013	02/2019	02/2020	242.09	410.00	167.91	12
99	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	03/2025	651.00	1009.00	358	120
100	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	12/2018	08/2020	258.20	358.68	100.48	20
101	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	03/2022	548.00	819.01	271.01	24
102	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	09/2021	569.63	670.00	100.37	18
103	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	03/2019	03/2020	314.00	728.00	414	12
104	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2020	632.68	816.55	183.87	57
105	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	ER	04/1987	03/2006	03/2025	406.99	545.70	138.71	228
106	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	03/2025	915.98	2137.81	1221.83	36
107	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	01/2020	295.00	477.31	182.31	12
108	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	MRTP	03/2013	03/2016	06/2021	4874.58	8574.97	3700.39	63
109	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	12/2019	02/2021	246.08	348.55	102.47	14
110	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	03/2022	320.66	858.96	538.3	36
111	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	12/2024	2912.96	3845.60	932.64	33
112	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	ER	04/2005	03/2017	03/2025	595.51	769.40	173.89	96

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

526

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
113	KOTTAVALSA - KORAPUT DOUBLING	ECOR	04/2015	03/2022	03/2024	2499.71	3382.95	883.24	24
114	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	03/2022	701.61	810.02	108.41	40
115	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	03/2021	969.83	1312.96	343.13	12
116	BONDAMUNDA RANCHI DOUBLING	SER	03/2016	03/2021	12/2021	1724.20	1993.24	269.04	9
117	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	03/2030	1027.40	2373.00	1345.6	324
118	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	03/2020	644.78	890.00	245.22	36
119	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	12/2022	2288.00	4970.11	2682.11	9

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
120	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MoRTH	08/2010	09/2014	06/2020	186.96	305.61	118.65	69
121	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	NHAI	11/2012	07/2018	02/2020	605.84	722.46	116.62	19
122	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	NHAI	08/2016	09/2019	03/2020	1388.34	2587.50	1199.16	6
123	FOUR LANING OF CHANDIGARH - KHARAR	NHAI	10/2015	12/2017	06/2020	447.29	746.43	299.14	30
124	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	09/2020	531.13	727.00	195.87	28
125	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	NHAI	09/2016	08/2019	12/2020	950.69	1108.00	157.31	16
126	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	03/2021	1288.07	1420.00	131.93	12
127	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	03/2020	1108.00	2967.50	1859.5	100
128	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	MoRTH	11/2010	03/2011	12/2020	624.41	992.67	368.26	117

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

527

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JANUARY 2020)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
129	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MoRTH	08/2010	10/2010	06/2021	193.69	327.92	134.23	128
130	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	MoRTH	08/2010	10/2010	06/2020	195.04	377.99	182.95	116
131	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	05/2021	1124.11	1232.76	108.65	44
132	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	MoRTH	11/2013	05/2017	05/2020	497.05	881.05	384	36
133	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	MoRTH	11/2011	09/2015	10/2021	954.43	1191.51	237.08	73
134	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	06/2020	1928.22	2945.00	1016.78	62

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
135	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	07/2020	1,5525.00	2,3140.00	7615	62

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
136	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	05/2020	1,3334.00	2,4664.00	11330	58

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
137	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	03/2020	5181.79	6218.14	1036.35	32
138	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	CPWD	02/2014	05/2017	03/2020	388.00	490.00	102	34
139	REDEVELOPMENT OF EAST KIDWAI NAGAR	NBCC	06/2012	11/2019	05/2020	4264.00	4720.73	456.73	6
140	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	03/2021	1219.21	2000.00	780.79	17

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

528

TOR -> Time Overrun

**DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS
OF RS.100 CRORE AND ABOVE**

(JANUARY 2020)

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipa ted	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
141	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	12/2021	1,0151.04	5,5548.87	45397.8	21

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

COR -> Cost Overrun

Details of Ongoing Projects Under -Public Private Partnership Mode

Annexure-XVIII

Costing Rs. 150 Crore and above					(January 2020)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>National Highways Authority Of India</u>							
1	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - PPP (BOT) - [N24000208]	07/2012	291.36 -	291.36	01/2014 -	-	.00	0
2	GWALIOR-JHANSI, NH-75 - PPP (ANNUITY) - [N24000089]	12/2003	604.00 -	364.59	12/2009 -	03/2020	-39.64	123
3	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - PPP (ANNUITY) - [N24000176]	05/2010	374.00 -	374.00	05/2013 -	-	.00	0
4	INDORE-DEWAS(NH-3) - PPP (BOT) - [N24000159]	11/2010	325.00 -	475.00	05/2013 -	-	46.15	0
5	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - PPP (ANNUITY) - [N24000177]	09/2011	485.00 -	485.00	08/2013 -	-	.00	0
6	DELHI/ HARYANA BORDER TO ROHTAK - PPP (BOT) - [N24000122]	04/2007	486.00 -	486.00	05/2010 -	03/2020	.00	118
7	TRICHY - KARUR - PPP (BOT) - [N24000528]	03/2007	516.00 -	516.00	07/2008 -	-	.00	0
8	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - PPP (BOT) - [N24000426]	11/2012	530.07 -	530.07	08/2016 -	06/2020	.00	46
9	TIRUPATI - TIRUTHANI - CHENNAI - PPP (BOT) - [N24000178]	04/2011	571.00 -	571.00	10/2013 -	-	.00	0
10	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - PPP (BOT) - [N24000185]	09/2011	574.00 -	574.00	03/2014 -	-	.00	0
11	4-LANNING OF CHAPRA-HAJIPUR - PPP (ANNUITY) - [N24000187]	01/2011	575.00 -	575.00	07/2013 -	03/2020	.00	80
12	2 LANNING OF MUZAFFARPUR - SONBARSA - PPP (ANNUITY) - [N24000188]	05/2011	511.54 -	591.00	11/2013 -	03/2020	15.53	76
13	SIX LANNING OF VADAKKANANCHERRY THRISSURESECTION KM 240 270KM - PPP (BOT) - [N24000149]	02/2010	617.00 -	617.00	08/2012 -	12/2019	.00	88
14	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - PPP (ANNUITY) - [N24000213]	04/2012	624.00 -	624.00	04/2014 -	-	.00	0
15	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - PPP (BOT) - [N24000586]	06/2016	637.18 -	637.18	06/2019 -	09/2019	.00	3
16	PATNA-MUZAFFARPUR - PPP (ANNUITY) - [N24000165]	08/2010	671.30 -	671.30	02/2013 -	03/2020	.00	85
17	MUZAFFARNAGAR-HARIDWAR - PPP (BOT) - [N24000201]	09/2011	754.00 -	754.00	03/2013 -	11/2020	.00	92

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above					(January 2020)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
18	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - PPP (BOT) - [N24000587]	06/2016	763.23 -	763.23	06/2019 -	11/2019	.00	5
19	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - PPP (BOT) - [N24000445]	08/2014	822.90 -	822.90	04/2018 -	-	.00	0
20	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - PPP (BOT) - [N24000454]	06/2014	923.04 -	923.04	11/2016 -	05/2020	.00	42
21	KANDLA - MUNDRA PORT - PPP (BOT) - [N24000175]	01/2011	953.88 -	953.88	07/2013 -	11/2020	.00	88
22	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - PPP (BOT) - [N24000453]	01/2015	972.50 -	972.50	07/2017 -	03/2020	.00	32
23	4-LANING OF BRAHAMPUR-FARAKA - PPP (BOT) - [N24000203]	02/2011	998.79 -	998.79	08/2013 -	03/2021	.00	91
24	BAREILLY-SITAPUR (NH-24) - PPP (BOT) - [N24000200]	03/2011	1,046.00 -	1,046.00	09/2013 -	-	.00	0
25	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - PPP (BOT) - [N24000205]	12/2011	1,047.00 -	1,047.00	06/2014 -	03/2019	.00	57
26	4-LANING OF FARAKA-RAIGANJ - PPP (BOT) - [N24000202]	02/2011	1,078.84 -	1,078.84	08/2013 -	05/2020	.00	81
27	SRINAGAR TO BANIHAL - PPP (ANNUITY) - [N24000189]	06/2011	1,100.70 -	1,100.70	06/2014 -	10/2020	.00	76
28	GHAZIABAD-ALIGARH NH-91 - PPP (BOT) - [N24000170]	02/2011	1,141.00 -	1,141.00	08/2013 -	-	.00	0
29	INDORE-JHABUA-GUJRAT/MP - PPP (BOT) - [N24000136]	10/2010	1,175.00 -	1,175.00	04/2013 -	-	.00	0
30	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - PPP (BOT) - [N24000172]	09/2011	1,250.00 -	1,250.00	12/2013 -	06/2020	.00	78
31	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - PPP (BOT) - [N24000230]	05/2013	1,348.20 -	1,348.20	02/2014 -	-	.00	0
32	FOUR LANING OF HOSPET - CHITRADURGA - PPP (BOT) - [N24000490]	03/2015	1,388.00 -	1,388.00	08/2018 -	03/2020	.00	19
33	6-LANING OF DHANKUNI-KHARAGPUR SECTION - PPP (BOT) - [N24000206]	04/2012	1,396.18 -	1,396.18	09/2014 -	03/2020	.00	66
34	PANIKHOLI-RIMOLI - PPP (BOT) - [N24000197]	03/2012	1,410.00 -	1,410.00	09/2014 -	-	.00	0
35	RANCHI-RARGA-JAMSETHPUR - PPP (ANNUITY) - [N24000215]	12/2012	1,479.00 -	1,479.00	06/2015 -	-	.00	0
36	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - PPP (BOT) - [N24000125]	03/2010	1,509.10 -	1,509.10	09/2012 -	-	.00	0
37	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - PPP (BOT) - [N24000183]	11/2011	1,535.00 -	1,535.00	05/2014 -	03/2020	.00	70

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above (January 2020)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
38	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 (BOT) - [N24000233] - PPP	04/2014	1,266.60	1,544.00	09/2016	-	21.90	0
39	ETAWAH CHAKERI - PPP (BOT) - [N24000219]	03/2013	1,573.00	1,573.00	09/2015	-	.00	0
40	FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - PPP (BOT) - [N24000505]	06/2015	1,583.79	1,583.79	01/2019	10/2019	.00	9
41	FOUR LANING OF GWALIOR-SHIVPURI - PPP (BOT) - [N24000494]	05/2013	1,055.00	1,601.77	11/2015	-	51.83	0
42	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - PPP (BOT) - [N24000462]	05/2014	1,655.01	1,655.01	08/2016	12/2020	.00	52
43	6 LANING OF AGRA - ETAWAH BYPASS - PPP (BOT) - [N24000452]	07/2015	1,657.20	1,657.20	01/2019	-	.00	0
44	SIX-LANING OF BARWA ADDA-PANAGARH - PPP (BOT) - [N24000515]	04/2014	1,665.00	1,665.00	-	-	.00	0
45	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - PPP (BOT) - [N24000477]	02/2008	1,673.70	1,673.70	10/2011	-	.00	0
46	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - PPP (BOT) - [N24000131]	02/2009	1,693.75	1,693.75	08/2011	-	.00	0
47	PUNE-SATARA(NH-4) - PPP (BOT) - [N24000156]	10/2010	1,724.55	1,724.55	03/2013	03/2020	.00	84
48	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - PPP (ANNUITY) - [N24000163]	07/2010	1,813.76	1,813.76	07/2013	-	.00	0
49	FOUR LANING OF AURANGABAD - YEDISHI - PPP (BOT) - [N24000508]	07/2015	1,871.34	1,871.34	01/2018	03/2020	.00	26
50	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - PPP (BOT) - [N24000232]	11/2013	1,916.79	1,916.79	11/2016	-	.00	0
51	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - PPP (ANNUITY) - [N24000161]	07/2010	1,987.00	1,987.00	07/2015	09/2020	.00	62
52	AHMEDABAD TO VADODARA SECTION - PPP (BOT) - [N24000222]	01/2013	2,125.24	2,125.24	12/2015	-	.00	0
53	8 LANING OF MUKARBA CHOWK TO PANIPAT - PPP (BOT) - [N24000449]	07/2015	2,128.72	2,128.72	04/2019	-	.00	0
54	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH – 14 - PPP BOT (Hybrid Annuity) - [N24001185]	11/2017	2,159.00	2,159.00	01/2019	-	.00	0
55	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - PPP (BOT) - [N24000425]	07/2015	2,288.18	2,288.18	05/2019	-	.00	0
56	4 LANING OF NAGPUR-BETUL - PPP (ANNUITY) - [N24000155]	02/2011	2,498.76	2,498.76	08/2014	-	.00	0
57	NASHRI- CHANANI - PPP (ANNUITY) - [N24000162]	05/2011	2,159.00	2,519.00	06/2015	-	16.67	0
58	VARANASI-AURANGABAD KM.786 TO KM.978.40 - PPP (BOT) - [N24000182]	09/2011	2,848.00	2,848.00	03/2014	06/2020	.00	75

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above (January 2020)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
59	DELHI AGRA APPROVED LENGTH 180.0 KM - PPP (BOT) - [N24000224]	10/2012	1,928.22 -	2,945.00	04/2015 -	06/2020	52.73	62
60	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - PPP (BOT) - [N24000133]	05/2009	1,108.00 -	2,967.50	11/2011 -	03/2020	167.82	100
	Total		74,864.42 -	78,914.92				
	Grand Total		74,864.42	78,914.92				

State-wise Central Sector Ongoing Projects Details

Annexure-XIX

Details of Central Sector Projects Costing Rs.150 crore and above (as on 31.01.2020)					
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	A & N ISLANDS				
	Civil Aviation				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	9/2018 (-) [6/2020]	314.61 (-) [441.33]	85.79 (126.72) [21]
	Road Transport And Highways				
2	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N	3/2017	12/2017 (-) [0/0]	409.85 (-) [409.85]	21.11 (0.00) [0]
3	AJANTHA TO BULDHANA	2/2017	7/2019 (-) [7/2019]	401.00 (401.00) [401.00]	121.81 (0.00) [0]
4	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C	3/2015	4/2017 (-) [0/0]	277.17 (-) [277.17]	159.49 (0.00) [0]
5	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (	3/2015	10/2018 (-) [0/0]	262.97 (-) [262.97]	0.00 (0.00) [0]
6	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	11/2017	11/2019 (-) [0/0]	257.34 (-) [238.00]	41.09 (-19.34) [0]
7	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM	2/2018	10/2018 (-) [0/0]	391.00 (-) [391.00]	22.17 (0.00) [0]
8	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O	3/2018	10/2018 (-) [0/0]	234.27 (-) [234.27]	11.03 (0.00) [0]
9	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00	11/2017	11/2019 (-) [0/0]	237.80 (-) [238.00]	7.48 (0.20) [0]
	ANDHRA PRADESH				
	Health And Family Welfare				
10	HOSPITAL AND TEACHING- AIIMS GUNTUR	3/2018	/ (-) [7/2020]	601.02 (-) [601.02]	219.05 (0.00) [-]
11	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS- MNAGLAGIRI GUNTUR, ANDHRA PRADESH	8/2017	3/2019 (-) [3/2020]	272.19 (-) [272.54]	204.08 (0.35) [12]
	Petroleum				
12	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE	1/2015	3/2021 (-) [3/2021]	342.00 (-) [342.00]	0.00 (0.00) [0]
13	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH	8/2018	4/2021 (-) [7/2021]	466.00 (-) [466.00]	124.36 (0.00) [3]
14	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP	8/2017	4/2021 (-)	384.58 (-)	134.67 (0.00)

			[9/2020]	[384.58]	[-7]
15	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT	7/2017	2/2021 (-) [2/2021]	580.20 (-) [580.20]	66.56 (0.00) [0]
16	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	3/2016	6/2020 (-) [8/2021]	34,012.00 (-) [34,012.00]	4,995.31 (0.00) [14]
17	LPG BP PROJECT CHITTOOR	7/2019	7/2022 (-) [7/2022]	167.00 (-) [167.00]	3.62 (0.00) [0]
18	REVAMPING OF FACILITIES AT VIZAG TERMINAL	4/2018	4/2022 (-) [2/2023]	355.00 (-) [355.00]	29.38 (0.00) [10]
19	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM	7/2014	3/2021 (-) [3/2021]	247.00 (-) [247.00]	0.00 (0.00) [0]
20	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP	10/2018	10/2021 (-) [10/2021]	316.20 (-) [316.20]	18.83 (0.00) [0]
21	SWRO II WITH LLPH FACILITIES	9/2019	7/2020 (-) [7/2020]	196.26 (-) [196.26]	0.00 (0.00) [0]
22	VISAKH REFINERY MODERNISATION PROJECT	7/2016	7/2020 (7/2022) [7/2022]	20,928.00 (26,264.00) [26,264.00]	8,584.07 (5,336.00) [24]
	<u>Railways</u>				
23	CUMBUM-PRODDATUR	4/2013	/ (-) [0/0]	829.00 (829.00) [829.00]	0.94 (0.00) [0]
24	DUVVADA-VIJAYAWADA	4/2015	/ (-) [0/0]	3,873.07 (3,873.07) [3,873.07]	0.38 (0.00) [0]
25	GUDUR-DURGARAJPATNAM	4/2011	/ (-) [0/0]	761.37 (761.37) [761.37]	0.52 (0.00) [0]
26	GUNTUR-GUNTAKAL	4/2016	3/2022 (-) [3/2023]	3,631.00 (3,631.00) [3,631.00]	678.02 (0.00) [12]
27	KOTLPALLI-NARASAPUR (NL) (SCR)	12/2001	3/2009 (-) [3/2023]	1,045.20 (2,120.16) [2,120.16]	561.18 (1,074.96) [168]
28	KOTTAVALSA - KORAPUT DOUBLING	4/2015	3/2022 (3/2024) [3/2024]	2,499.71 (2,499.71) [3,382.95]	447.56 (883.24) [24]
29	MULTI MODAL LOGISTICS PARK AT KAKINADA	8/2016	3/2019 (-) [12/2020]	234.50 (-) [235.00]	10.88 (0.50) [21]
30	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM	1/2013	3/2018 (-) [0/0]	387.70 (-) [387.70]	323.91 (0.00) [0]
31	NADIKUDE-SRI KALAHASTI	4/2011	3/2021 (-) [3/2024]	2,288.70 (2,643.25) [2,643.25]	860.07 (354.55) [36]
32	NANDYAL-YERRAGUNTLA(NL),SCR	3/1996	2/2009 (-) [0/0]	164.36 (-) [1,050.00]	999.64 (885.64) [0]
33	VIJAYAWADA-GUDUR	4/2015	12/2023 (-) [12/2023]	3,246.26 (-) [3,548.67]	1,384.54 (302.41) [0]
34	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	3/2012	3/2020 (-)	1,503.71 (-)	1,966.03 (696.29)

			[3/2022]	[2,200.00]	[24]
	Road Transport And Highways				
35	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM	12/2017	/ (-) [0/0]	328.67 (-) [328.67]	206.07 (0.00) [0]
36	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O	12/2017	/ (-) [0/0]	357.00 (-) [357.00]	70.71 (0.00) [0]
37	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415	3/2018	/ (6/2020) [6/2020]	557.30 (-) [557.30]	211.24 (0.00) [-]
38	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216	1/2017	9/2017 (12/2020) [12/2020]	263.45 (-) [263.45]	60.26 (0.00) [39]
39	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V	2/2017	11/2017 (3/2020) [3/2020]	429.43 (-) [429.43]	255.68 (0.00) [28]
40	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1	3/2018	/ (-) [12/2020]	314.43 (-) [314.43]	46.12 (0.00) [-]
41	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD	8/2016	1/2017 (4/2020) [4/2020]	350.61 (-) [350.61]	310.25 (0.00) [39]
42	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C	10/2015	11/2015 (-) [0/0]	333.21 (-) [353.89]	256.11 (20.68) [0]
43	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C	7/2015	12/2015 (-) [0/0]	333.21 (333.21) [333.21]	256.11 (0.00) [0]
44	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0)	7/2015	12/2015 (-) [0/0]	333.21 (-) [333.21]	256.11 (0.00) [0]
45	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12	10/2015	12/2015 (1/2020) [1/2020]	333.21 (-) [355.89]	294.81 (22.68) [49]
46	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)	3/2018	3/2021 (-) [4/2021]	1,532.62 (2,499.00) [2,499.00]	730.93 (966.38) [1]
47	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40)	6/2017	6/2017 (-) [8/2020]	648.33 (-) [306.00]	157.33 (-342.33) [38]
48	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800)	1/2016	11/2018 (-) [0/0]	1,134.97 (-) [1,134.97]	806.94 (0.00) [0]
49	REHABILITAITON AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH	1/2017	1/2018 (12/2020) [1/2020]	576.48 (-) [576.48]	237.30 (0.00) [24]
50	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT	1/2016	8/2016 (3/2020) [3/2020]	348.95 (-) [348.95]	169.46 (0.00) [43]
51	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S	7/2014	2/2015 (-) [0/0]	251.55 (-) [251.55]	7.74 (0.00) [0]
52	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21	1/2016	5/2016 (12/2019) [5/2018]	386.09 (-) [386.09]	184.26 (0.00) [0]
53	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69	11/2016	5/2017 (3/2020) [3/2020]	290.15 (-) [290.15]	73.11 (0.00) [34]
54	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR	1/2014	11/2014 (-)	195.45 (-)	0.00 (0.00)

	DAM T		[0/0]	[195.45]	[0]
55	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS	3/2018	/ (-) [2/2021]	565.09 (-) [565.09]	191.77 (0.00) [-]
56	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O	3/2016	5/2016 (7/2020) [7/2020]	995.09 (995.00) [995.09]	419.22 (0.00) [50]
57	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216	3/2016	9/2016 (3/2020) [3/2020]	444.84 (-) [444.84]	273.88 (0.00) [42]
58	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2	11/2016	8/2017 (2/2020) [2/2020]	376.25 (-) [376.25]	228.69 (0.00) [30]
59	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (	3/2018	7/2018 (1/2020) [1/2020]	297.12 (294.00) [294.12]	373.98 (-3.00) [18]
60	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG	3/2018	8/2018 (2/2020) [2/2020]	289.67 (290.00) [289.67]	105.02 (0.00) [18]
61	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA	3/2018	11/2018 (5/2020) [5/2020]	504.19 (504.00) [504.19]	248.37 (0.00) [18]
62	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES	3/2015	10/2015 (1/2020) [1/2020]	271.45 (-) [271.45]	182.45 (0.00) [51]
63	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD	1/2017	8/2017 (3/2020) [3/2020]	319.28 (-) [319.28]	111.98 (0.00) [31]
64	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER	3/2017	3/2020 (-) [3/2020]	648.32 (-) [511.94]	511.34 (-136.38) [0]
65	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU	3/2018	8/2018 (2/2020) [2/2020]	244.95 (245.00) [244.95]	136.22 (0.00) [18]
66	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU	9/2016	2/2017 (12/2019) [2/2019]	372.68 (-) [372.68]	185.04 (0.00) [0]
67	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3	3/2018	8/2018 (3/2020) [3/2020]	228.32 (-) [228.32]	48.15 (0.00) [19]
68	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P	1/2018	8/2018 (8/2020) [8/2020]	418.03 (-) [418.03]	194.62 (0.00) [24]
69	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO	11/2016	1/2018 (1/2020) [1/2020]	378.24 (-) [378.24]	307.17 (0.00) [24]
70	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM	2/2018	/ (-) [7/2021]	1,959.00 (-) [1,959.00]	706.39 (0.00) [-]
71	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN	12/2017	/ (-) [7/2021]	1,323.15 (-) [1,323.15]	403.93 (0.00) [-]
72	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG	3/2018	/ (-) [7/2021]	1,550.98 (1,730.07) [1,550.98]	786.78 (0.00) [-]
73	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	11/2011	5/2014 (12/2019) [3/2020]	1,535.00 (-) [1,535.00]	3,260.65 (0.00) [70]
74	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	3/2017	3/2020 (-) [5/2020]	1,041.62 (-) [1,187.10]	829.16 (145.48) [2]

75	TIRUPATI - TIRUTHANI - CHENNAI	4/2011	10/2013 (-) [0/0]	571.00 (-) [571.00]	582.53 (0.00) [0]
76	VIJAYAWADA-GUNDUGOLANU SECTION	9/2014	2/2017 (-) [0/0]	1,684.00 (-) [1,684.00]	54.13 (0.00) [0]
	<u>Steel</u>				
77	CENTRAL DISPATCH YARD	8/2015	8/2018 (2/2020) [2/2020]	320.66 (-) [320.66]	257.04 (0.00) [18]
78	COKE OVEN BATTERY-5	12/2011	12/2017 (3/2020) [3/2020]	2,858.00 (-) [2,500.00]	1,535.76 (-358.00) [27]
	<u>Urban Development</u>				
79	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P.	2/2019	9/2020 (-) [9/2020]	186.00 (199.00) [186.00]	38.35 (0.00) [0]
80	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUDEM AP	1/2018	3/2019 (-) [0/0]	206.58 (-) [206.58]	185.77 (0.00) [0]
81	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA	7/2014	/ (-) [0/0]	232.00 (-) [232.00]	0.00 (0.00) [0]
82	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	8/2007	/ (-) [0/0]	246.90 (-) [246.90]	0.00 (0.00) [0]
	<u>Water Resources</u>				
83	POLAVARAM IRRIGATION PROJECT	2/2009	3/2020 (11/2019) [12/2021]	10,151.04 (55,548.87) [55,548.87]	32,535.80 (45,397.83) [21]
	<u>ARUNACHAL PRADESH</u>				
	<u>Power</u>				
84	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009 (6/2020) [6/2020]	2,496.90 (7,927.34) [7,927.34]	7,743.76 (5,430.44) [126]
85	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (8/2023) [8/2023]	6,285.33 (-) [19,496.34]	11,842.12 (13,211.01) [155]
	<u>Road Transport And Highways</u>				
86	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN	3/2015	/ (-) [0/0]	172.75 (-) [172.75]	120.18 (0.00) [0]
87	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	3/2015	6/2018 (-) [3/2020]	394.00 (-) [394.00]	325.08 (0.00) [21]
88	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59	3/2015	5/2018 (-) [8/2019]	194.11 (-) [194.11]	181.03 (0.00) [0]
89	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS	10/2015	1/2019 (-) [0/0]	179.82 (-) [179.82]	197.77 (0.00) [0]
90	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX	10/2015	/ (1/2016) [1/2019]	210.50 (210.50) [210.50]	122.09 (0.00) [0]
91	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROM KM.583.450	1/2016	11/2016 (-) [0/0]	183.65 (-) [183.65]	129.11 (0.00) [0]
92	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST	11/2016	/ (-) [9/2020]	243.89 (-) [243.89]	128.46 (0.00) [-]
93	BORDUMSA NAMCHIK (BURIDEHING - JAIRAMPUR) ROAD	7/2015	/	189.91	154.43

	ON NH-52B (NEW NH-215) FROM KM. 0.15 (STARTING CHAIN		(-) [0/0]	(-) [189.91]	(0.00) [0]
94	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 37.500 TO KM	5/2016	/	259.52	184.51
			(-) [0/0]	(-) [259.52]	(0.00) [0]
95	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120.	12/2016	/	200.44	79.80
			(-) [0/0]	(-) [200.44]	(0.00) [0]
96	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50	9/2016	/	568.92	172.88
			(-) [0/0]	(-) [568.92]	(0.00) [0]
97	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5	12/2016	/	188.78	59.98
			(-) [0/0]	(-) [188.78]	(0.00) [0]
98	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	12/2016	1/2017	138.93	79.91
			(-) [1/2020]	(155.00) [155.00]	(16.07) [36]
99	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37	4/2016	/	245.79	129.43
			(-) [9/2020]	(-) [245.79]	(0.00) [-]
100	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM.	4/2016	10/2016	198.00	184.62
			(-) [10/2019]	(-) [198.00]	(0.00) [0]
101	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH	7/2015	10/2018	197.16	81.53
			(9/2015) [9/2018]	(197.16) [197.16]	(0.00) [0]
102	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF	3/2017	/	1,718.59	204.77
			(-) [0/0]	(-) [1,718.59]	(0.00) [0]
103	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	1/2017	3/2017	1,253.10	204.77
			(-) [3/2022]	(-) [1,253.10]	(0.00) [60]
104	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	2/2017	4/2017	167.28	21.54
			(2/2018) [2/2021]	(167.28) [167.28]	(0.00) [46]
105	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS	2/2017	4/2017	216.71	25.17
			(2/2018) [2/2021]	(216.71) [216.71]	(0.00) [46]
106	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K	3/2018	/	392.60	0.00
			(-) [0/0]	(-) [392.60]	(0.00) [0]
107	FUNDED)CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH	11/2015	/	434.06	172.89
			(-) [12/2020]	(-) [434.06]	(0.00) [-]
108	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017	284.09	96.13
			(3/2018) [3/2021]	(284.09) [284.09]	(0.00) [47]
109	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017	195.23	62.01
			(-) [0/0]	(-) [195.23]	(0.00) [0]
110	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	2/2017	4/2017	203.36	72.88
			(-) [0/0]	(-) [203.36]	(0.00) [0]
111	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017	194.66	84.11
			(-) [0/0]	(-) [194.66]	(0.00) [0]
112	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017	198.22	84.11
			(-) [0/0]	(-) [198.22]	(0.00) [0]
113	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00)	3/2012	5/2012	207.03	308.09
			(5/2015)	(389.45)	(182.42)

	IN ARUNACHAL PR		[12/2019]	[389.45]	[0]
114	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	2/2017	4/2017 (2/2018) [2/2021]	180.57 (180.57) [180.57]	16.80 (0.00) [46]
115	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS	2/2017	4/2017 (2/2018) [2/2021]	168.32 (168.32) [168.32]	40.78 (0.00) [46]
116	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	12/2011	2/2012 (-) [0/0]	156.63 (276.00) [276.00]	147.65 (119.37) [0]
117	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P	11/2010	3/2011 (-) [0/0]	305.49 (-) [305.49]	131.08 (0.00) [0]
118	TWO-LANING OF HAYULIANG– HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI	1/2017	/ (-) [0/0]	256.66 (-) [256.66]	24.14 (0.00) [0]
119	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0	2/2017	/ (4/2019) [4/2022]	175.06 (175.06) [175.06]	29.08 (0.00) [-]
120	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1	2/2017	/ (4/2019) [4/2022]	176.12 (176.12) [176.12]	28.16 (0.00) [-]
121	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D	2/2017	/ (2/2018) [2/2021]	199.02 (199.02) [199.02]	13.82 (0.00) [-]
122	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D	2/2017	/ (2/2018) [2/2021]	184.88 (184.88) [184.88]	7.68 (0.00) [-]
123	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU	9/2011	/ (3/2020) [0/0]	1,979.00 (-) [1,979.00]	1,189.58 (0.00) [0]
	<u>ASSAM</u>				
	<u>Civil Aviation</u>				
124	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	3/2021 (-) [3/2021]	859.86 (-) [860.00]	232.44 (0.14) [0]
	<u>Health And Family Welfare</u>				
125	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021 (8/2021) [10/2021]	875.00 (-) [747.80]	137.27 (-127.20) [5]
	<u>Petroleum</u>				
126	BS VI PROJECT AT GUWAHATI REFINERY	8/2018	2/2020 (-) [4/2020]	557.00 (-) [557.00]	313.62 (0.00) [2]
127	BS-VI PROJECT AT BONGAIGAON REFINERY	5/2018	9/2019 (-) [2/2020]	1,222.00 (-) [1,222.00]	739.04 (0.00) [5]
128	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN	6/2016	8/2020 (-) [8/2020]	224.75 (-) [224.75]	98.98 (0.00) [0]
129	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	7/2011	1/2019 (-) [0/0]	350.00 (-) [350.00]	2.06 (0.00) [0]
130	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	6/2016	8/2019 (-) [12/2020]	423.00 (-) [423.00]	363.66 (0.00) [16]
131	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (-) [6/2020]	543.91 (-) [682.90]	71.46 (138.99) [4]
132	INDMAX PROJECT AT BONGAIGAON REFINERY	2/2016	11/2019 (-)	2,582.00 (-)	1,704.47 (0.00)

			[2/2020]	[2,582.00]	[3]
133	NUMALIGARH REFINERY EXPANSION PROJECT	1/2019	10/2024 (-) [10/2024]	22,594.00 (-) [22,594.00]	43.00 (0.00) [0]
134	PIPELINE NETWORK PROJECT GELEKI, ASSAM	7/2016	5/2020 (-) [5/2020]	249.85 (265.49) [265.49]	152.67 (15.64) [0]
135	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	9/2012	3/2015 (-) [0/0]	871.35 (-) [1,200.00]	565.63 (328.65) [0]
	<u>Railways</u>				
136	AMBARI FALAKATA TO NEW MAYNAGURI	4/2011	3/2019 (-) [3/2020]	314.00 (728.00) [728.00]	731.27 (414.00) [12]
137	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-) [3/2020]	2,232.32 (-) [2,182.00]	765.94 (-50.32) [-24]
138	DIGARU-HOJAI (102 KM)	4/2015	3/2021 (-) [3/2021]	870.96 (-) [2,136.01]	610.95 (1,265.05) [0]
139	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [3/2020]	385.20 (1,532.00) [1,532.00]	652.15 (1,146.80) [12]
	<u>Road Transport And Highways</u>				
140	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (-) [0/0]	268.08 (-) [268.08]	203.15 (0.00) [0]
141	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	11/2010	2/2011 (-) [0/0]	470.20 (-) [630.36]	386.98 (160.16) [0]
142	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS	12/2015	12/2018 (-) [0/0]	225.02 (-) [159.20]	26.00 (-65.82) [0]
143	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	12/2015	6/2018 (-) [0/0]	223.30 (-) [223.30]	84.69 (0.00) [0]
144	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-) [0/0]	520.01 (-) [520.01]	56.63 (0.00) [0]
145	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [0/0]	588.95 (-) [588.95]	403.00 (0.00) [0]
146	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [0/0]	289.99 (-) [289.99]	15.37 (0.00) [0]
147	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (12/2021) [0/0]	252.00 (-) [252.00]	11.04 (0.00) [0]
148	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	6/2018 (12/2020) [12/2021]	437.39 (-) [437.39]	10.01 (0.00) [42]
149	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	1/2016 (2/2019) [4/2021]	294.17 (-) [294.17]	76.25 (0.00) [63]
150	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	4/2010 (-) [7/2019]	217.61 (-) [360.84]	454.21 (143.23) [0]
151	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM	11/2010	2/2014 (-) [12/2019]	197.37 (-) [197.37]	88.86 (0.00) [0]
152	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	5/2008	160.00	223.81

			(-) [6/2019]	(-) [167.98]	(7.98) [0]
153	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52	6/2016	1/2019 (-) [0/0]	829.00 (-) [829.00]	311.84 (0.00) [0]
154	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [0/0]	168.39 (-) [168.39]	84.69 (0.00) [0]
155	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE	10/2017	/ (-) [6/2020]	818.00 (-) [818.00]	63.08 (0.00) [-]
156	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5	6/2015	6/2018 (1/2021) [12/2021]	463.49 (-) [463.49]	26.15 (0.00) [42]
157	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	3/2015	1/2016 (-) [0/0]	829.00 (-) [829.00]	311.86 (0.00) [0]
158	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (5/2020) [12/2020]	454.89 (-) [454.89]	141.83 (0.00) [31]
159	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	2/2009 (7/2019) [7/2019]	280.00 (520.00) [520.00]	492.41 (240.00) [0]
160	HARANGAJO TO MAIBANG, NH-54	12/2003	7/2009 (10/2018) [10/2018]	196.00 (655.17) [655.17]	655.17 (459.17) [0]
161	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008 (1/2011) [8/2013]	155.04 (255.23) [255.23]	251.39 (100.19) [0]
162	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	4/2009 (3/2011) [8/2019]	199.81 (340.14) [340.14]	319.96 (140.33) [0]
163	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008 (7/2011) [1/2014]	167.64 (435.78) [435.78]	427.96 (268.14) [0]
164	NALBARI T BIJNI (AS-7)	12/2003	4/2008 (-) [3/2020]	208.00 (-) [230.00]	340.21 (22.00) [143]
165	NALBARI TO BIJNI (AS-6)	12/2003	6/2008 (-) [9/2019]	225.00 (-) [225.00]	328.47 (0.00) [0]
166	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST	3/2017	/ (-) [0/0]	1,049.51 (-) [1,049.51]	89.16 (0.00) [0]
167	SONAPUR TO GUWAHTI (AS-3)	12/2003	3/2008 (-) [8/2020]	245.00 (-) [174.34]	225.65 (-70.66) [149]
168	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ	11/2014	2/2018 (-) [0/0]	218.31 (-) [307.47]	263.85 (89.16) [0]
169	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN	9/2018	9/2021 (-) [9/2021]	160.00 (-) [160.00]	0.50 (0.00) [0]
	<u>BIHAR</u>				
	<u>Civil Aviation</u>				
170	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II	5/2018	10/2022 (-) [10/2022]	539.20 (-) [539.20]	25.64 (0.00) [0]
	<u>Petroleum</u>				
171	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL	5/2016	12/2020 (-)	664.00 (-)	664.73 (65.40)

			[2/2020]	[729.40]	[-10]
172	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA	10/2017	10/2022 (-) [10/2022]	359.25 (-) [359.25]	81.40 (0.00) [0]
173	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR	4/2018	3/2021 (-) [3/2021]	522.00 (-) [522.00]	187.36 (0.00) [0]
174	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY	12/2017	10/2020 (-) [10/2020]	199.36 (-) [199.36]	9.39 (0.00) [0]
175	FUEL QUALITY UPGRADATION (NSU,NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY	6/2017	10/2019 (-) [5/2020]	951.64 (-) [951.64]	552.00 (0.00) [7]
176	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY	7/2018	1/2021 (-) [1/2021]	189.00 (-) [189.00]	33.25 (0.00) [0]
177	LPG BP PROJECT MOTIHARI	5/2018	3/2021 (-) [3/2021]	206.50 (-) [206.50]	38.09 (0.00) [0]
178	MOTIHARI AMLEKHGANJ PIPELINE	9/2015	6/2020 (-) [3/2020]	324.00 (-) [324.00]	199.72 (0.00) [-3]
	<u>Power</u>				
179	BARH STPP(3X660MW) NTPC	2/2005	10/2011 (8/2021) [8/2021]	8,692.97 (21,312.11) [21,312.11]	16,928.07 (12,619.14) [118]
180	BRBCL-NABINAGAR TPP- JV (4X250 MW)	1/2007	7/2012 (-) [9/2020]	5,353.00 (7,998.00) [9,583.00]	8,056.25 (4,230.00) [98]
181	BUXAR THERMAL POWER PLANT (1320 MW)	3/2019	1/2024 (-) [1/2024]	10,439.09 (10,439.09) [10,439.09]	876.79 (0.00) [0]
182	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	1/2013	5/2018 (12/2021) [6/2021]	12,964.60 (17,304.00) [17,304.00]	14,367.00 (4,339.40) [37]
	<u>Railways</u>				
183	ARA-BHABHUA ROAD (NL)	4/2008	/ (-) [0/0]	633.87 (-) [633.87]	0.40 (0.00) [0]
184	ARARIA-SUPAUL (NL)	4/2008	/ (3/2023) [3/2023]	1,605.17 (1,605.17) [1,605.17]	23.55 (0.00) [-]
185	BIHTA-AURANGABAD (NL)	4/2008	/ (-) [3/2024]	326.20 (-) [2,995.01]	1.94 (2,668.81) [-]
186	CHHAPRA-MUZAFFARPUR (NL)	4/2006	/ (-) [3/2022]	378.56 (-) [1,858.75]	377.77 (1,480.19) [-]
187	DANIAWAN-BIHARSARIF (NL), ECR	4/2001	/ (-) [0/0]	406.92 (-) [339.00]	200.00 (-67.92) [0]
188	DARBANGHA-KUSHESHWARSTHAN (NL)	4/2005	/ (-) [0/0]	205.00 (-) [205.00]	5.21 (0.00) [0]
189	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	4/1991	/ (-) [12/2021]	329.39 (803.11) [1,483.14]	1,060.33 (1,153.75) [-]
190	GAYA-DALTONGANJ VIA RAFIGANJ (NL)	4/2008	/ (-) [0/0]	445.25 (-) [445.25]	1.15 (0.00) [0]
191	HAJIPUR-RAMDAYALUNAGAR DOUBLING	4/2013	/	213.01	432.20

			(-) [1/2020]	(367.17) [440.00]	(226.99) [-]
192	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	4/2003	/	528.65	1,454.19
			(-) [3/2023]	(2,066.78) [2,066.78]	(1,538.13) [-]
193	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	4/1997	3/2012	324.73	1,041.96
			(-) [3/2020]	(898.53) [1,050.00]	(725.27) [96]
194	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	4/2009	3/2020	548.00	525.18
			(-) [3/2022]	(819.01) [819.01]	(271.01) [24]
195	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	4/1997	/	162.87	311.33
			(-) [3/2022]	(614.45) [614.45]	(451.58) [-]
196	KISHANGANJ JALALGARH, NL, NEFR	4/2008	/	333.76	6.74
			(3/2022) [3/2022]	(-) [360.00]	(26.24) [-]
197	KIUL - GAYA DOUBLING PROJECT	12/2015	3/2020	1,200.20	586.83
			(-) [10/2021]	(1,200.20) [1,200.20]	(0.00) [19]
198	KOSI BRIDGE (NL), ECR	4/2002	3/2020	499.41	404.10
			(-) [3/2020]	(516.02) [516.02]	(16.61) [0]
199	KURSELA-BIHARIGANJ (NL)	4/2008	/	192.56	0.39
			(-) [0/0]	(-) [192.56]	(0.00) [0]
200	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	4/1996	3/2012	477.88	674.58
			(-) [3/2020]	(751.55) [751.55]	(273.67) [96]
201	MOTIHARI-SITAMARHI (NL)	4/2006	/	211.00	24.16
			(-) [0/0]	(-) [1,006.00]	(795.00) [0]
202	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM	4/2016	3/2021	731.64	60.65
			(-) [3/2022]	(1,185.73) [1,185.73]	(454.09) [12]
203	MUZAFFARPUR-DARBANGHA (NL)	4/2008	/	281.30	0.60
			(-) [0/0]	(-) [281.30]	(0.00) [0]
204	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL)	4/2008	/	228.05	1.53
			(-) [3/2024]	(-) [228.05]	(0.00) [-]
205	MUZAFFARPUR-SITAMARHI NEW LINE	1/1991	7/2014	332.15	541.43
			(-) [0/0]	(546.71) [546.71]	(214.56) [0]
206	NAWADA-LAXMIPUR (NL)	4/2008	/	620.57	0.31
			(-) [0/0]	(-) [620.57]	(0.00) [0]
207	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	9/2006	3/2019	532.87	935.62
			(-) [3/2020]	(2,145.00) [2,145.00]	(1,612.13) [12]
208	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR	4/1998	/	180.82	521.48
			(-) [10/2019]	(726.31) [726.31]	(545.49) [0]
209	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	12/2015	3/2020	1,491.47	448.67
			(-) [12/2021]	(-) [1,491.47]	(0.00) [21]
210	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM	4/2016	3/2021	744.04	156.95
			(-) [3/2022]	(1,215.54) [1,215.54]	(471.50) [12]
211	SAKRI-HASANPUR ROAD (NL)	4/1999	/	325.00	367.62
			(-)	(735.20)	(410.20)

			[3/2021]	[735.20]	[-]
212	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	4/2004	/	372.14	849.10
			(-)	(1,470.50)	(1,098.36)
			[3/2021]	[1,470.50]	[-]
213	SAMASTIPUR-DARBANGHA	5/2015	/	380.00	195.83
			(-)	(519.33)	(139.33)
			[2/2023]	[519.33]	[-]
214	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)	4/2008	/	678.62	17.20
			(-)	(-)	(0.00)
			[0/0]	[678.62]	[0]
	Road Transport And Highways				
215	2 LANNING OF MUZAFFARPUR - SONBARSA	5/2011	11/2013	511.54	571.86
			(12/2019)	(585.00)	(79.46)
			[3/2020]	[591.00]	[76]
216	2-LANNING WITH PS MOTIHARI-RAXAUL	10/2011	4/2014	375.09	494.33
			(-)	(-)	(0.00)
			[0/0]	[375.09]	[0]
217	4-LANNING OF CHAPRA-HAJIPUR	1/2011	7/2013	575.00	850.24
			(-)	(-)	(0.00)
			[3/2020]	[575.00]	[80]
218	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ	5/2015	5/2017	581.84	89.69
			(-)	(-)	(0.00)
			[4/2019]	[581.84]	[0]
219	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00	2/2019	/	2,926.42	0.00
			(-)	(-)	(0.00)
			[0/0]	[2,926.42]	[0]
220	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND	9/2018	/	1,478.40	0.00
			(-)	(-)	(0.00)
			[0/0]	[1,478.40]	[0]
221	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE	8/2015	11/2015	288.24	286.46
			(-)	(-)	(0.00)
			[0/0]	[288.24]	[0]
222	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15	12/2017	/	2,598.00	0.00
			(-)	(-)	(0.00)
			[0/0]	[2,598.00]	[0]
223	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE	3/2017	3/2020	235.48	11.00
			(-)	(-)	(-7.71)
			[5/2021]	[227.77]	[14]
224	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER	3/2018	/	496.20	0.00
			(-)	(-)	(0.00)
			[0/0]	[496.20]	[0]
225	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	11/2013	7/2016	683.83	597.00
			(-)	(-)	(-123.13)
			[0/0]	[560.70]	[0]
226	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016	178.85	40.44
			(-)	(-)	(-26.23)
			[0/0]	[152.62]	[0]
227	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	6/2016	369.77	0.00
			(-)	(-)	(0.00)
			[0/0]	[369.77]	[0]
228	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016	553.30	289.14
			(-)	(-)	(-74.95)
			[0/0]	[478.35]	[0]
229	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31	12/2015	/	1,167.45	113.26
			(-)	(-)	(0.00)
			[12/2019]	[1,167.45]	[0]
230	FOUR LANING OF BHOJPUR TO BUXAR	1/1991	/	642.41	402.94
			(-)	(-)	(39.26)
			[10/2020]	[681.67]	[-]
231	FOUR LANING OF FORBESGANJ - JOGBANI	8/2015	4/2018	322.09	77.53
			(-)	(-)	(0.00)

			[12/2020]	[322.09]	[32]
232	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR	1/2014	10/2016 (-) [0/0]	1,408.85 (-) [925.87]	586.18 (-482.98) [0]
233	FOUR LANING OF KOILWAR TO BHOJPUR	8/2015	/ (-) [1/2020]	814.04 (-) [825.17]	646.72 (11.13) [-]
234	FOUR LANING OF PATNA TO KOILWAR	8/2015	/ (-) [0/0]	556.07 (-) [556.07]	0.00 (0.00) [0]
235	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31	12/2015	4/2019 (-) [0/0]	1,041.10 (-) [1,041.10]	214.34 (0.00) [0]
236	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	9/2011	3/2014 (-) [0/0]	574.00 (-) [574.00]	768.73 (0.00) [0]
237	PATNA-MUZZAFFARPUR	8/2010	2/2013 (-) [3/2020]	671.30 (-) [671.30]	1,132.48 (0.00) [85]
238	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM	8/2016	12/2016 (-) [0/0]	1,742.01 (-) [1,742.01]	1,034.37 (0.00) [0]
239	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I	1/2018	/ (-) [0/0]	573.70 (-) [573.70]	0.00 (0.00) [0]
240	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH	10/2013	8/2014 (-) [0/0]	278.39 (-) [278.39]	0.00 (0.00) [0]
241	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	1/1991	/ (-) [0/0]	478.35 (-) [478.35]	0.00 (0.00) [0]
242	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	1/1991	/ (-) [0/0]	319.68 (-) [369.77]	113.67 (50.09) [0]
243	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING	2/2014	7/2016 (-) [0/0]	665.50 (-) [665.50]	0.00 (0.00) [0]
244	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	1/1991	8/2016 (-) [0/0]	282.41 (-) [322.01]	278.45 (39.60) [0]
245	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	1/1991	10/2016 (-) [0/0]	358.22 (-) [377.64]	325.19 (19.42) [0]
246	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	1/1991	/ (-) [0/0]	675.00 (-) [675.00]	154.56 (0.00) [0]
247	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHI KM 40	1/1991	/ (-) [0/0]	154.62 (-) [154.62]	0.00 (0.00) [0]
248	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION	1/2018	/ (-) [0/0]	895.39 (-) [895.39]	0.00 (0.00) [0]
249	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	8/2017	8/2017 (-) [2/2022]	950.64 (-) [950.64]	102.51 (0.00) [54]
250	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH	3/2018	/ (-) [0/0]	153.24 (-) [153.24]	2.06 (0.00) [0]
251	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPR	3/2015	7/2016 (-) [0/0]	206.80 (-) [206.80]	74.04 (0.00) [0]

252	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA	8/2015	4/2019 (-) [0/0]	399.54 (-) [297.27]	509.75 (-102.27) [0]
253	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ	8/2015	/	854.80 (-) [854.80]	558.04 (0.00) [0]
254	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR	8/2015	4/2018 (-) [0/0]	516.13 (-) [516.13]	395.25 (0.00) [0]
255	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN	3/2017	3/2020 (-) [3/2020]	672.89 (-) [736.01]	0.00 (63.12) [0]
256	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC	5/2014	8/2016 (-) [12/2020]	199.98 (-) [199.98]	153.43 (0.00) [52]
257	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C	11/2016	10/2019 (-) [0/0]	230.34 (-) [230.34]	178.39 (0.00) [0]
<u>Urban Development</u>					
258	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	2/2016	6/2017 (-) [3/2021]	496.18 (496.00) [498.99]	118.00 (2.81) [45]
259	IRRIGATION WORK OF BAGMATI	10/2005	3/2015 (-) [3/2021]	956.00 (-) [956.00]	651.21 (0.00) [72]
<u>Water Resources</u>					
260	I AND D AND STP AT CHAPRA	11/2018	12/2020 (-) [12/2020]	236.15 (-) [236.15]	0.06 (0.00) [0]
261	I AND D AND STP WORKS FOR BHAGALPUR	10/2017	9/2020 (-) [9/2020]	254.13 (-) [254.13]	0.05 (0.00) [0]
262	SAIDPUR SEWER NETWORK PATNA	4/2015	1/2021 (-) [1/2021]	268.63 (-) [268.63]	192.80 (0.00) [0]
263	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR	4/2015	4/2020 (-) [4/2020]	184.93 (-) [184.93]	163.36 (0.00) [0]
264	SEWER NETWORK SPS AND STP BEGUSARAI	3/2018	7/2021 (-) [7/2021]	230.06 (-) [230.06]	0.00 (0.00) [0]
265	SEWER NETWORKS SPS AND STP HAJIPUR	3/2018	8/2021 (-) [8/2021]	305.19 (-) [305.19]	0.00 (0.00) [0]
266	SEWER NETWORKS, SPS AND STP, MUNGER	3/2018	10/2021 (-) [10/2021]	294.02 (-) [294.02]	0.00 (0.00) [0]
267	SEWERAGE SCHEME AT PAHARI ZONE IVA S PATNA	5/2017	5/2021 (-) [5/2021]	184.86 (-) [184.86]	103.13 (0.00) [0]
268	SEWERAGE SCHEME AT PAHARI ZONE V PATNA	5/2017	4/2021 (-) [4/2021]	356.37 (-) [356.37]	66.44 (0.00) [0]
269	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA	8/2017	6/2022 (-) [6/2022]	824.00 (-) [824.00]	0.41 (0.00) [0]
270	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA	8/2017	6/2022 (-) [6/2022]	578.89 (-) [578.89]	0.29 (0.00) [0]
271	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	3/2020 (-)	225.77 (-)	183.57 (0.00)

			[3/2020]	[225.77]	[0]
272	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK	3/2017	5/2021 (-) [5/2021]	277.42 (-) [277.42]	85.87 (0.00) [0]
273	SEWERAGE TREATMENT PLANT AT PAHARI PATNA	5/2017	11/2020 (-) [11/2020]	191.62 (-) [191.62]	37.70 (0.00) [0]
	<u>CHANDIGARH</u>				
	<u>Road Transport And Highways</u>				
274	WIDENING OF SL TO 2 L KM. 107-184.80 SUKUMA TO KONTA ON NH 221	3/2010	3/2013 (-) [0/0]	179.89 (271.00) [271.00]	0.00 (91.11) [0]
275	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1	12/2010	1/2019 (-) [0/0]	169.26 (299.00) [299.00]	0.00 (129.74) [0]
	<u>CHHATISGARH</u>				
	<u>Coal</u>				
276	AMERA OC RCE	2/2015	3/2018 (-) [3/2020]	335.97 (-) [335.97]	51.21 (0.00) [24]
277	AMGAON OPENCAST PROJECT RCE	7/2015	3/2020 (-) [3/2020]	316.10 (-) [316.10]	88.82 (0.00) [0]
278	BAROUD OC EXPANSION (RCE)- 3MTY	4/2012	3/2016 (-) [3/2020]	258.56 (-) [258.56]	182.04 (0.00) [48]
279	BIJARI OC RCE (1.50 MTY)	5/2014	3/2020 (-) [3/2020]	164.49 (-) [164.49]	81.59 (0.00) [0]
280	CHHAL OC SEAM -III (6.00 MTY)	12/2013	3/2022 (-) [3/2022]	610.63 (-) [610.63]	110.31 (0.00) [0]
281	DURGAPUR OPENCAST PROJECT	2/2015	3/2023 (-) [3/2023]	916.24 (-) [916.24]	4.94 (0.00) [0]
282	GEVRA EXPANSION OCP (SECL) (35-70) MTY	6/2010	3/2023 (3/2016) [3/2023]	11,816.40 (-) [11,816.40]	2,920.18 (0.00) [0]
283	JAGANNATHPOR OCP(3.00MTY)	9/2008	3/2015 (3/2020) [3/2020]	152.43 (459.49) [459.49]	195.34 (307.06) [60]
284	JHIRIA WEST OPENCAST PROJECT	11/2018	3/2026 (-) [3/2026]	389.97 (-) [389.97]	0.00 (0.00) [0]
285	KARTALI (EAST) OCP (2.50 MTY)	7/2008	3/2014 (-) [3/2020]	178.44 (-) [178.44]	2.92 (0.00) [72]
286	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY	8/2013	3/2023 (-) [3/2023]	7,612.33 (-) [7,612.33]	2,358.32 (0.00) [0]
287	MADANNAGAR OPENCAST PROJECT	10/2015	3/2024 (-) [3/2024]	1,875.32 (-) [1,875.32]	0.00 (0.00) [0]
288	MAHAMAYA OPENCAST PROJECT	5/2018	3/2026 (-) [3/2026]	410.26 (-) [410.26]	9.53 (0.00) [0]
289	MANIKPUR OC EXPANSION (3.5 MTY)	12/2009	3/2014 (-) [3/2021]	321.50 (-) [321.50]	197.36 (0.00) [84]
290	PELMA OCP(15.00MTY)	11/2014	3/2023 (-)	1,624.59 (-)	6.58 (0.00)

			[3/2023]	[1,624.59]	[0]
291	VIJAY WEST OPENCAST PROJECT	5/2017	3/2026 (-) [3/2026]	976.95 (-) [976.95]	75.96 (0.00) [0]
	<u>Power</u>				
292	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	12/2012	10/2017 (3/2020) [3/2020]	11,846.00 (-) [12,739.82]	12,826.56 (893.82) [29]
293	TALAIPALLI COAL MINING PROJECT	9/2015	11/2019 (-) [11/2019]	3,004.00 (-) [3,004.00]	1,813.00 (0.00) [0]
	<u>Railways</u>				
294	CHAMPA-JHARSUGUDA 3RD LINE	4/2008	12/2019 (3/2020) [3/2020]	872.00 (1,226.51) [1,226.51]	1,066.54 (354.51) [3]
295	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW	2/2016	3/2020 (-) [3/2020]	393.98 (-) [393.98]	290.45 (0.00) [0]
296	GEVRA ROAD PENDRA ROAD	2/2014	3/2022 (-) [12/2022]	2,288.00 (-) [4,970.11]	635.13 (2,682.11) [9]
297	JHARSUGUDA-BILASPUR 4TH LINE	4/2015	3/2021 (3/2023) [3/2023]	1,973.00 (1,973.64) [1,973.64]	185.98 (0.64) [24]
298	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	4/2013	9/2018 (-) [3/2021]	3,055.00 (-) [3,055.00]	2,096.39 (0.00) [30]
299	KIRANDUL - JAGDALPUR DOUBLING	12/2012	3/2020 (3/2023) [3/2023]	1,160.00 (1,160.83) [1,160.83]	749.76 (0.83) [36]
300	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR	5/2014	3/2018 (-) [0/0]	207.00 (-) [207.00]	153.83 (0.00) [0]
301	RAIPUR - TITLAGARH - DOUBLING	3/2007	3/2020 (-) [12/2020]	1,402.02 (-) [1,100.00]	1,122.87 (-302.02) [9]
	<u>Road Transport And Highways</u>				
302	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF	3/2018	/ (3/2021) [3/2021]	1,029.96 (-) [1,261.05]	97.55 (231.09) [-]
303	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1)	12/2015	4/2018 (3/2020) [3/2020]	726.67 (598.13) [598.13]	414.73 (-128.54) [23]
304	FOUR LANING OF SARAGAON - BILASPUR	12/2015	4/2018 (8/2018) [8/2018]	509.13 (-) [509.13]	412.66 (0.00) [0]
305	FOUR LANING OF SIMGA - SARAGAON	12/2015	5/2018 (10/2019) [10/2019]	596.67 (-) [596.67]	405.42 (0.00) [0]
306	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION.	12/2015	/ (-) [0/0]	291.05 (-) [291.05]	182.16 (0.00) [0]
307	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION	11/2015	6/2017 (-) [0/0]	335.32 (-) [335.32]	214.60 (0.00) [0]
308	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 127.500 TO 178.944 DARRIGHAT TO BANARI SECTION	3/2016	9/2016 (-) [0/0]	491.52 (-) [491.52]	473.67 (0.00) [0]
309	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V	1/2016	9/2016 (-) [0/0]	476.20 (544.00) [544.00]	372.74 (67.80) [0]

310	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION	12/2014	3/2015 (-) [0/0]	496.02 (-) [496.02]	225.69 (0.00) [0]
311	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180	1/2016	8/2016 (-) [0/0]	497.14 (-) [497.14]	187.31 (0.00) [0]
312	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	1/2016	10/2016 (-) [0/0]	624.98 (-) [624.98]	253.27 (0.00) [0]
313	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI	3/2016	7/2016 (-) [0/0]	452.94 (-) [452.94]	66.25 (0.00) [0]
314	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO	3/2017	1/2018 (-) [0/0]	423.79 (-) [423.79]	158.78 (0.00) [0]
315	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION	11/2015	12/2015 (-) [0/0]	485.44 (-) [485.44]	447.13 (0.00) [0]
316	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A	11/2017	5/2019 (-) [0/0]	188.80 (-) [188.80]	0.00 (0.00) [0]
317	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331	12/2014	11/2017 (-) [0/0]	379.16 (-) [379.16]	0.00 (0.00) [0]
	<u>Steel</u>				
318	NMDC INTEGRATED STEEL PLANT	1/2010	5/2015 (7/2020) [7/2020]	15,525.00 (23,140.00) [23,140.00]	16,468.33 (7,615.00) [62]
	<u>D & N HAVELI</u>				
	<u>Petroleum</u>				
319	DAMAN DEVELOPMENT PROJECT	8/2014	5/2019 (3/2020) [3/2020]	6,086.08 (5,842.31) [5,842.31]	4,784.88 (-243.77) [10]
	<u>DELHI</u>				
	<u>Civil Aviation</u>				
320	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	11/2016	4/2020 (-) [12/2020]	233.38 (-) [233.38]	84.73 (0.00) [8]
	<u>Commerce And Industry</u>				
321	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	12/2019 (-) [9/2020]	4,773.00 (-) [5,178.00]	1,309.65 (405.00) [9]
	<u>Health And Family Welfare</u>				
322	AIIMS - MOTHER AND CHILD BLOCK	12/2013	5/2017 (-) [6/2020]	204.44 (-) [270.00]	210.75 (65.56) [37]
323	AIIMS - OPD(NEW)	8/2014	5/2017 (-) [1/2020]	293.65 (-) [325.00]	304.62 (31.35) [32]
324	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	/ (-) [5/2020]	156.56 (-) [156.64]	80.28 (0.08) [-]
325	LHMC NEW DELHI-RE-DEVELOPMENT	2/2013	11/2013 (-) [9/2020]	414.11 (-) [499.23]	337.32 (85.12) [82]
	<u>Heavy Industry</u>				
326	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	8/2016	9/2019 (-) [3/2020]	1,554.00 (-) [1,554.00]	716.25 (0.00) [6]
	<u>Power</u>				
327	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF	3/2015	5/2017	1,394.52	457.17

	DELHI DURING 12TH PLAN PERIOD (PART-A)		(6/2019) [3/2020]	(-) [1,394.52]	(0.00) [34]
	<u>Railways</u>				
328	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE	4/2012	/ (-) [3/2023]	295.68 (-) [295.68]	92.91 (0.00) [-]
329	GRADE SEPERATOR AT DAYABASTI	4/1999	/ (-) [3/2024]	156.65 (-) [197.17]	106.97 (40.52) [-]
	<u>Road Transport And Highways</u>				
330	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8	7/2017	9/2019 (-) [0/0]	269.69 (-) [269.69]	0.00 (0.00) [0]
	<u>Telecommunications</u>				
331	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	6/2016	6/2017 (-) [0/0]	418.26 (-) [418.26]	367.04 (0.00) [0]
	<u>Urban Development</u>				
332	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	6/2015	4/2019 (-) [12/2020]	197.33 (-) [197.33]	67.09 (0.00) [20]
333	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI	7/2017	/ (-) [0/0]	218.72 (218.72) [218.72]	57.71 (0.00) [0]
334	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	7/2012	12/2015 (-) [0/0]	884.30 (-) [884.30]	746.48 (0.00) [0]
335	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	10/2017	11/2019 (8/2020) [8/2020]	271.90 (-) [271.90]	65.00 (0.00) [9]
336	CONSTRUCTION OF GRAMEEN VIKAS BHAWAN (2BASEMENTS+ GROUND+9 FLOORS) FOR MINISTRY OF RURAL DEVELOPMENT	11/2018	7/2021 (-) [7/2021]	361.60 (-) [361.60]	0.45 (0.00) [0]
337	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS	7/2019	3/2025 (-) [3/2025]	24,948.65 (-) [24,948.65]	78.44 (0.00) [0]
338	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND	5/2017	12/2020 (-) [12/2020]	565.00 (-) [565.00]	420.66 (0.00) [0]
339	DELHI MRTS PHASE-III	9/2011	3/2016 (-) [0/0]	38,585.00 (-) [38,585.00]	34,763.00 (0.00) [0]
340	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	10/2019 (-) [3/2021]	1,219.21 (-) [2,000.00]	436.20 (780.79) [17]
341	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B	11/2017	5/2020 (-) [5/2020]	238.56 (-) [238.56]	63.67 (0.00) [0]
342	REDEVELOPMENT OF EAST KIDWAI NAGAR	6/2012	11/2019 (3/2020) [5/2020]	4,264.00 (4,720.73) [4,720.73]	4,553.13 (456.73) [6]
343	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I	10/2016	7/2021 (-) [7/2021]	1,180.00 (-) [1,100.80]	9.96 (-79.20) [0]
344	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N	10/2016	/ (8/2020) [3/2021]	392.00 (-) [392.00]	13.90 (0.00) [-]
345	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I	10/2016	3/2022 (-) [3/2022]	1,128.00 (-) [1,128.00]	1.52 (0.00) [0]
346	REDEVELOPMENT OF GPRA AT MOHAMMADPUR	10/2016	/	422.00	15.11

			(3/2021) [12/2020]	(-) [422.00]	(0.00) [-]
347	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR	7/2016	/	2,694.00	0.00
			(-) [0/0]	(-) [2,694.00]	(0.00) [0]
348	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	10/2016	4/2018 (2/2020) [8/2020]	248.20 (-) [248.20]	52.95 (0.00) [28]
	<u>Water Resources</u>				
349	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO	5/2017	5/2020 (-) [5/2020]	344.81 (-) [344.81]	0.00 (0.00) [0]
350	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI	12/2018	1/2021 (-) [1/2021]	515.07 (-) [515.07]	246.01 (0.00) [0]
351	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L	3/2017	12/2022 (-) [12/2022]	665.78 (-) [665.78]	94.40 (0.00) [0]
352	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2	5/2016	12/2021 (-) [12/2021]	211.79 (-) [211.79]	39.14 (0.00) [0]
353	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S	5/2016	2/2022 (-) [2/2022]	239.11 (-) [239.11]	42.77 (0.00) [0]
	<u>GOA</u>				
	<u>Health And Family Welfare</u>				
354	SUPER SPECIALITY BLOCK PMSSY GOA	1/2018	/	249.01	149.26
			(-) [5/2020]	(-) [249.07]	(0.06) [-]
	<u>Human Resource Development</u>				
355	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA.	5/2019	3/2020 (-) [3/2020]	303.90 (-) [303.90]	0.00 (0.00) [0]
	<u>Road Transport And Highways</u>				
356	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE	3/2015	/	280.16	219.47
			(-) [0/0]	(-) [290.59]	(10.43) [0]
357	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD	3/2015	/	184.05	96.58
			(-) [0/0]	(-) [184.05]	(0.00) [0]
358	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE	10/2015	/	936.40	262.25
			(-) [0/0]	(-) [936.40]	(0.00) [0]
359	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K	3/2015	/	298.33	160.33
			(-) [0/0]	(-) [298.33]	(0.00) [0]
360	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDEAPAR BRIDGE	3/2015	4/2018 (-) [0/0]	297.00 (-) [297.00]	290.64 (0.00) [0]
361	KARASWADA TO BAMBOLIM	3/2017	12/2019 (-) [12/2019]	852.67 (852.67) [852.67]	86.04 (0.00) [0]
362	PATRADEVI TO KARASWADA 4L	3/2017	5/2020 (-) [5/2020]	634.32 (634.32) [634.32]	109.33 (0.00) [0]
363	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER	12/2015	/	773.98	259.66
			(-) [0/0]	(-) [773.98]	(0.00) [0]
364	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR	12/2015	/	819.95	193.63
			(-) [0/0]	(-) [819.95]	(0.00) [0]

	<u>GUJARAT</u>				
	<u>Atomic Energy</u>				
365	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015 (-) [9/2021]	11,459.00 (-) [16,580.00]	14,629.00 (5,121.00) [69]
	<u>Petroleum</u>				
366	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY	11/2019	5/2023 (-) [5/2023]	5,251.00 (-) [5,251.00]	0.00 (0.00) [0]
367	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTA TO 2.5 MMTA AT KANDLA, GUJARAT	3/2018	/ (-) [8/2022]	588.20 (-) [588.20]	1.24 (0.00) [-]
368	BS-VI PROJECT AT GUJARAT REFINERY	3/2018	9/2019 (-) [2/2020]	3,380.00 (-) [3,380.00]	2,346.62 (0.00) [5]
369	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	4/2016	4/2018 (-) [2/2020]	327.78 (-) [200.00]	155.59 (-127.78) [22]
370	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY	8/2017	8/2020 (-) [8/2020]	1,342.00 (-) [1,342.00]	6.30 (0.00) [0]
371	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE	10/2017	2/2020 (-) [10/2020]	906.00 (-) [906.00]	123.94 (0.00) [8]
372	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY	9/2016	7/2020 (-) [7/2020]	208.35 (-) [208.35]	148.25 (0.00) [0]
373	LAB REVAMP AT GUJARAT REFINERY	10/2019	12/2021 (-) [12/2021]	403.00 (-) [403.00]	43.50 (0.00) [0]
374	REDEVELOPMENT OF SANTHAL FIELD	2/2017	3/2026 (-) [3/2026]	1,162.56 (-) [1,162.56]	441.61 (0.00) [0]
375	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI	9/2018	2/2021 (-) [2/2021]	225.54 (-) [225.54]	2.44 (0.00) [0]
	<u>Power</u>				
376	SUPPLEMENTARY TRANS. SYSTEM FOR UMSP AT BANASKANTHA (RADHANESDA) GUJARAT	12/2017	6/2019 (3/2020) [3/2020]	193.14 (-) [193.14]	102.44 (0.00) [9]
377	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT	5/2017	9/2018 (3/2020) [3/2020]	175.64 (-) [175.64]	106.20 (0.00) [18]
	<u>Railways</u>				
378	AHMEDABAD-BOTAD (GC)	4/2012	12/2021 (-) [12/2021]	975.62 (-) [1,082.32]	1,202.24 (106.70) [0]
379	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	4/2008	3/2020 (3/2021) [3/2021]	829.74 (1,215.34) [1,310.23]	1,532.69 (480.49) [12]
380	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	4/2006	3/2011 (-) [3/2017]	117.36 (196.95) [202.35]	809.40 (84.99) [0]
381	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	2/1991	3/2019 (3/2020) [3/2020]	551.51 (809.07) [809.07]	635.52 (257.56) [12]
382	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	4/2008	3/2012 (3/2022) [3/2022]	318.24 (321.62) [321.62]	125.76 (3.38) [120]
383	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM	4/2017	3/2020 (3/2021)	691.84 (663.29)	199.24 (-28.55)

			[3/2021]	[663.29]	[12]
384	DHASA-JETALSAR (GC)	4/2012	3/2021 (-) [3/2021]	644.38 (-) [644.38]	507.11 (0.00) [0]
385	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO	3/2017	/ (-) [0/0]	243.60 (-) [243.60]	0.00 (0.00) [0]
386	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC)	4/2011	/ (3/2021) [3/2021]	844.10 (844.10) [844.10]	110.71 (0.00) [-]
387	MULTI MODAL LOGISTICS PARK AT VARNAMA	10/2013	3/2019 (-) [0/0]	343.00 (-) [343.00]	222.83 (0.00) [0]
388	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220	3/2012	/ (-) [0/0]	153.83 (-) [153.83]	0.00 (0.00) [0]
389	PALANPUR-SAMAKHAYALI (DL)	4/2013	12/2021 (-) [3/2022]	1,548.66 (-) [1,548.66]	1,421.83 (0.00) [3]
390	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	4/1994	3/2019 (3/2022) [3/2022]	320.66 (858.56) [858.96]	534.00 (538.30) [36]
391	SURENDRA NAGAR RAJKOT	4/2015	3/2021 (3/2021) [3/2021]	1,002.39 (1,002.39) [1,002.39]	454.02 (0.00) [0]
392	VIRAMGAM-SAMAKHIALI (DL)	4/2011	3/2021 (3/2022) [3/2022]	1,037.15 (1,037.15) [1,037.15]	1,035.89 (0.00) [12]
393	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON	3/2012	/ (-) [0/0]	248.26 (-) [248.26]	0.00 (0.00) [0]
	Road Transport And Highways				
394	2-LANE WITH PAVED SHOULDERS OF GADU- PORBANDER SECTION	12/2016	/ (-) [9/2019]	417.19 (-) [417.19]	264.05 (0.00) [0]
395	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH- 8E FROM KM 221.610 TO KM 263.000	7/2016	/ (-) [1/2020]	829.97 (-) [829.97]	194.67 (0.00) [-]
396	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT	6/2017	6/2020 (2/2018) [2/2021]	1,958.88 (1,993.81) [1,993.81]	1,116.85 (34.93) [8]
397	AHMEDABAD TO VADODARA SECTION	1/2013	12/2015 (-) [0/0]	2,125.24 (2,125.24) [2,125.24]	4,669.71 (0.00) [0]
398	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS	5/2016	/ (-) [8/2020]	364.56 (-) [392.00]	286.99 (27.44) [-]
399	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR	3/2018	/ (11/2021) [0/0]	1,161.39 (1,404.00) [1,161.39]	0.00 (0.00) [0]
400	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S	3/2018	/ (12/2018) [7/2021]	1,437.64 (1,687.00) [1,437.64]	564.11 (0.00) [-]
401	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S	3/2018	/ (5/2018) [1/2021]	2,702.05 (-) [2,043.00]	0.00 (-659.05) [-]
402	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA	10/2018	5/2019 (-) [0/0]	400.76 (-) [400.76]	64.52 (0.00) [0]
403	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN	8/2017	3/2018 (-)	962.43 (-)	115.08 (0.00)

	THE STATE OF GU		[0/0]	[962.43]	[0]
404	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE	12/2017	11/2018 (-) [0/0]	867.97 (-) [867.97]	232.58 (0.00) [0]
405	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6.	5/2016	/ (-) [0/0]	998.18 (-) [998.18]	441.80 (0.00) [0]
406	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST	5/2016	/ (-) [0/0]	723.64 (-) [723.64]	313.19 (0.00) [0]
407	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR	5/2016	/ (-) [0/0]	834.64 (-) [834.64]	319.33 (0.00) [0]
408	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU	5/2016	/ (-) [0/0]	763.08 (-) [763.08]	391.13 (0.00) [0]
409	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	3/2010	9/2012 (12/2019) [0/0]	1,509.10 (3,787.21) [1,509.10]	3,684.44 (0.00) [0]
410	JUNAGADH BYPASS	10/2017	10/2017 (-) [11/2019]	232.49 (-) [232.49]	0.00 (0.00) [0]
411	KANDLA - MUNDRA PORT	1/2011	7/2013 (11/2020) [11/2020]	953.88 (-) [953.88]	976.79 (0.00) [88]
412	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF	2/2018	/ (-) [1/2021]	1,052.21 (1,449.00) [1,449.00]	342.39 (396.79) [-]
413	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG.	1/2017	/ (-) [1/2021]	1,251.11 (-) [1,251.11]	1,084.26 (0.00) [-]
414	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME	5/2016	/ (-) [0/0]	425.60 (241.41) [425.60]	105.83 (0.00) [0]
415	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4	3/2018	6/2021 (-) [6/2021]	351.00 (-) [351.00]	0.49 (0.00) [0]
416	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEEN	3/2018	11/2018 (-) [0/0]	464.07 (-) [464.07]	166.81 (0.00) [0]
417	UPGRADATION TO 2 LANE WITH PAVED SHOULDER WITH RIGID PAVEMENTS FROM 37/400 TO KM 66/700 ON NH 848 ON	3/2016	2/2016 (-) [0/0]	208.34 (-) [208.34]	112.87 (0.00) [0]
418	VADODARA-SURAT SECTION	3/2014	8/2016 (-) [10/2017]	503.16 (-) [503.16]	389.50 (0.00) [0]
419	WIDENING FROM TWO LANE TO FOUR LANE WITH PAVED SHOULDER AND STRENGTHNING OF EXISTING PAVEMENT BETWEEN	3/2016	2/2017 (-) [0/0]	223.67 (-) [223.67]	112.81 (0.00) [0]
	<u>Urban Development</u>				
420	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	12/2018 (-) [7/2020]	10,773.00 (-) [10,773.00]	6,532.69 (0.00) [19]
421	AHMEDABAD METRO RAIL PROJECT PHASE II	3/2019	3/2024 (-) [3/2024]	5,384.17 (-) [5,384.17]	4.35 (0.00) [0]
422	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT	1/2013	/ (-) [0/0]	175.00 (-) [175.00]	1.83 (0.00) [0]
423	SURAT METRO RAIL PROJECT	3/2019	3/2024 (-)	12,020.32 (-)	4.67 (0.00)

			[3/2024]	[12,020.32]	[0]
	<u>HARYANA</u>				
	<u>Fertilisers</u>				
424	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT	1/2018	11/2019 (-) [11/2019]	215.92 (-) [215.92]	134.50 (0.00) [0]
	<u>Health And Family Welfare</u>				
425	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	9/2014	3/2018 (-) [9/2019]	505.58 (-) [585.00]	586.96 (79.42) [0]
	<u>Petroleum</u>				
426	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY	1/2019	1/2021 (-) [8/2021]	909.00 (-) [909.00]	23.71 (0.00) [7]
427	BS-VI PROJECT AT PANIPAT REFINERY	12/2017	7/2019 (-) [2/2020]	3,529.00 (-) [3,529.00]	2,088.18 (0.00) [7]
428	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	4/2018	2/2020 (-) [12/2020]	206.63 (-) [206.63]	29.25 (0.00) [10]
429	COMPRESSED BIO GAS PLANT AT GORAKHPUR	9/2019	7/2021 (-) [7/2021]	164.69 (-) [164.69]	0.00 (0.00) [0]
430	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA	11/2017	11/2020 (-) [11/2020]	255.00 (-) [255.00]	128.36 (0.00) [0]
431	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY	10/2018	2/2020 (-) [1/2021]	598.00 (-) [598.00]	27.18 (0.00) [11]
432	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT	12/2018	6/2021 (-) [6/2021]	278.60 (-) [278.60]	0.00 (0.00) [0]
433	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT	8/2018	8/2020 (-) [8/2020]	1,636.00 (-) [1,636.00]	160.86 (0.00) [0]
434	PX-PTA REVAMP AT PANIPAT REFINERY	8/2019	10/2021 (-) [10/2021]	1,255.00 (-) [1,255.00]	106.50 (0.00) [0]
435	R and D CAMPUS II AT FARIDABAD	6/2019	12/2022 (-) [12/2022]	2,281.94 (-) [2,281.94]	0.00 (0.00) [0]
436	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT	8/2018	8/2020 (9/2020) [9/2020]	286.42 (-) [286.42]	6.18 (0.00) [1]
	<u>Railways</u>				
437	MULTI MODAL LOGISTICS PARK AT BARHI	12/2015	3/2019 (-) [3/2020]	346.32 (-) [346.32]	292.82 (0.00) [12]
438	ROHTAK-MEHAM HANSI	4/2012	12/2011 (-) [3/2021]	287.00 (695.00) [750.00]	290.62 (463.00) [111]
	<u>Road Transport And Highways</u>				
439	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	12/2015	6/2016 (-) [12/2019]	602.95 (507.70) [507.70]	496.22 (-95.25) [0]
440	4 LANING OF AMBALA - KAITHAL - PACKAGE -2	1/2016	7/2018 (-) [11/2019]	574.28 (537.16) [537.16]	514.61 (-37.12) [0]
441	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL	3/2017	3/2020 (-) [3/2020]	639.79 (-) [552.90]	578.15 (-86.89) [0]

442	8 LANING OF MUKARBA CHOWK TO PANIPAT	7/2015	4/2019 (-) [0/0]	2,128.72 (-) [2,128.72]	971.24 (0.00) [0]
443	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC)	1/2017	3/2019 (7/2019) [0/0]	276.01 (-) [276.01]	187.39 (0.00) [0]
444	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS	1/2017	3/2019 (6/2020) [6/2020]	247.25 (-) [247.25]	144.71 (0.00) [15]
445	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73	8/2016	5/2019 (-) [3/2020]	248.97 (-) [248.97]	249.15 (0.00) [10]
446	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P	3/2018	/ (-) [12/2020]	1,484.30 (-) [1,484.30]	133.06 (0.00) [-]
447	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211	9/2016	5/2019 (-) [2/2019]	1,004.67 (-) [813.45]	577.21 (-191.22) [0]
448	DELHI/ HARYANA BORDER TO ROHTAK	4/2007	5/2010 (-) [3/2020]	486.00 (-) [486.00]	470.01 (0.00) [118]
449	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2	11/2015	5/2018 (2/2018) [0/0]	867.66 (1,464.24) [1,464.24]	1,255.55 (596.58) [0]
450	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I	8/2015	2/2018 (10/2017) [0/0]	723.54 (1,286.84) [1,286.84]	1,163.65 (563.30) [0]
451	ISMAILABAD-NARNAUL PKG-1	1/2019	/ (-) [0/0]	996.65 (-) [996.65]	350.94 (0.00) [0]
452	ISMAILABAD-NARNAUL PKG-2	1/2019	/ (-) [0/0]	1,243.45 (-) [1,243.45]	405.84 (0.00) [0]
453	ISMAILABAD-NARNAUL PKG-3	1/2019	/ (-) [0/0]	889.36 (-) [889.36]	284.69 (0.00) [0]
454	ISMAILABAD-NARNAUL PKG-4	1/2019	/ (-) [0/0]	1,018.79 (-) [1,018.79]	267.69 (0.00) [0]
455	ISMAILABAD-NARNAUL PKG-5	1/2019	/ (-) [0/0]	1,051.91 (-) [1,051.91]	301.49 (0.00) [0]
456	ISMAILABAD-NARNAUL PKG-6	1/2019	/ (-) [0/0]	1,120.06 (-) [1,120.06]	250.18 (0.00) [0]
457	ISMAILABAD-NARNAUL PKG-7	1/2019	/ (-) [0/0]	1,137.42 (-) [1,137.42]	306.04 (0.00) [0]
458	ISMAILABAD-NARNAUL PKG-8	1/2019	/ (-) [0/0]	1,033.19 (-) [1,033.19]	209.75 (0.00) [0]
459	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	5/2009	11/2011 (-) [3/2020]	1,108.00 (2,967.50) [2,967.50]	3,990.72 (1,859.50) [100]
460	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS	3/2018	/ (-) [3/2020]	551.58 (-) [551.58]	305.46 (0.00) [-]
461	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE	3/2018	/ (-) [3/2020]	275.12 (-) [275.12]	134.80 (0.00) [-]
462	REHABILITATION AND UP-GRADATION FROM 2 LANE	3/2018	/	307.79	160.12

	WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTING		(-) [3/2020]	(-) [307.79]	(0.00) [-]
463	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN)	3/2018	/(-) [6/2020]	181.78 (-) [181.78]	76.56 (0.00) [-]
464	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN	3/2018	/(-) [3/2020]	198.05 (-) [198.05]	103.34 (0.00) [-]
465	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I)	3/2018	/(-) [7/2021]	795.50 (-) [799.30]	128.56 (3.80) [-]
466	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA	3/2018	/(-) [7/2021]	634.70 (931.21) [931.21]	143.54 (296.51) [-]
	HIMACHAL PRADESH				
	Health And Family Welfare				
467	AIIMS BILASPUR	4/2018	9/2021 (-) [9/2021]	1,351.00 (1,471.00) [1,471.00]	421.44 (120.00) [0]
	Power				
468	PARBATI HEP (4X200 MW) (NHPC) II	9/2002	9/2009 (12/2021) [12/2021]	3,919.59 (-) [9,997.11]	7,761.19 (6,077.52) [147]
	Railways				
469	BHANUPALI-BILASPUR BERTH	4/2008	12/2026 (-) [12/2025]	2,966.99 (-) [7,000.00]	472.83 (4,033.01) [-12]
	Road Transport And Highways				
470	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345)	2/2016	2/2019 (-) [6/2019]	273.20 (725.87) [273.20]	662.86 (0.00) [0]
471	4-LANING OF END OF PANDOH BYPASS TAKOLI IN H.P	6/2017	6/2020 (-) [9/2021]	2,485.93 (-) [2,485.93]	596.94 (0.00) [15]
472	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM)	11/2013	11/2016 (-) [0/0]	1,916.79 (-) [1,916.79]	1,948.92 (0.00) [0]
473	FOUR LANING OF PARWANOO -SOLAN	9/2015	3/2018 (-) [3/2020]	934.46 (-) [934.46]	586.91 (0.00) [24]
474	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M	3/2018	/(-) [5/2021]	478.74 (-) [478.74]	55.06 (0.00) [-]
475	FOUR LANING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH	9/2016	/(-) [7/2020]	1,273.71 (-) [1,273.71]	581.40 (0.00) [-]
476	FOUR LANING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000)	10/2016	/(-) [8/2020]	447.75 (-) [447.75]	1,028.99 (0.00) [-]
477	TWO LANING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS	8/2016	/(-) [9/2020]	1,583.18 (-) [1,583.18]	271.06 (0.00) [-]
	Urban Development				
478	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH	12/2018	6/2021 (-) [6/2021]	260.00 (-) [260.00]	12.50 (0.00) [0]
479	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	11/2012	11/2014 (-) [0/0]	270.83 (-) [270.83]	199.91 (0.00) [0]
	JAMMU AND KASHMIR				
	Civil Aviation				

480	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	7/2018	9/2021 (-) [9/2021]	323.19 (-) [323.19]	10.14 (0.00) [0]
	<u>Health And Family Welfare</u>				
481	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR	3/2019	9/2025 (-) [9/2025]	1,577.00 (-) [1,828.00]	0.00 (251.00) [0]
482	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR	3/2019	9/2023 (-) [9/2023]	1,404.00 (-) [1,404.00]	0.00 (0.00) [0]
	<u>Railways</u>				
483	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	3/1995	11/2002 (-) [6/2022]	2,500.00 (27,949.00) [27,949.00]	20,501.11 (25,449.00) [235]
	<u>Road Transport And Highways</u>				
484	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE	12/2017	/ (-) [1/2021]	1,471.75 (1,339.00) [1,339.00]	588.87 (-132.75) [-]
485	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A	12/2015	6/2019 (-) [12/2020]	2,168.66 (-) [2,168.66]	704.09 (0.00) [18]
486	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A	12/2015	12/2018 (-) [7/2020]	2,136.97 (-) [2,136.97]	1,248.94 (0.00) [19]
487	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	7/2010	7/2013 (-) [0/0]	1,813.76 (-) [1,813.76]	2,393.99 (0.00) [0]
488	NASHRI- CHANANI	5/2011	6/2015 (-) [0/0]	2,159.00 (-) [2,519.00]	4,707.04 (360.00) [0]
489	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	7/2010	7/2015 (12/2019) [9/2020]	1,987.00 (-) [1,987.00]	2,913.83 (0.00) [62]
490	SRINAGAR TO BANIHAL	6/2011	6/2014 (9/2017) [10/2020]	1,100.70 (-) [1,100.70]	2,898.41 (0.00) [76]
491	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA	3/2018	7/2019 (-) [0/0]	253.44 (-) [253.44]	0.00 (0.00) [0]
492	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0	3/2018	8/2018 (-) [0/0]	404.17 (-) [404.17]	53.66 (0.00) [0]
493	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM	3/2018	11/2018 (-) [0/0]	216.00 (-) [216.00]	21.23 (0.00) [0]
	<u>Urban Development</u>				
494	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C)	1/2018	/ (-) [0/0]	676.00 (-) [676.00]	0.00 (0.00) [0]
495	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1)	3/2019	/ (-) [0/0]	329.00 (-) [329.00]	0.00 (0.00) [0]
	<u>JHARKHAND</u>				
	<u>Coal</u>				
496	AMRAPALI OC(12MTY)	2/2012	3/2020 (-) [3/2020]	858.11 (-) [858.11]	190.41 (0.00) [0]
497	CHITRA EAST (RCE) OCP	8/2018	3/2024 (-) [3/2024]	513.98 (-) [513.98]	93.85 (0.00) [0]
498	CHURI BENTI UG (0.81 MTY)	8/2007	3/2011	163.51	107.16

			(-) [3/2021]	(-) [163.51]	(0.00) [120]
499	HURA - C OC (3 MTY)	10/2015	3/2022 (-) [3/2022]	359.69 (-) [359.69]	112.11 (0.00) [0]
500	KAPURIA UG(PSLW)	8/2011	4/2017 (-) [0/0]	988.35 (-) [988.35]	45.26 (0.00) [0]
501	KARMA OCP (1.0MTY)	6/2009	3/2014 (-) [3/2021]	162.46 (-) [162.46]	90.75 (0.00) [84]
502	MADHUBAND NLW WASHERY	8/2010	5/2014 (3/2020) [5/2020]	289.45 (-) [289.45]	263.37 (0.00) [72]
503	MAGADH OC 20 MTY (CCL)	8/2008	7/2012 (-) [3/2022]	706.40 (-) [706.40]	501.09 (0.00) [116]
504	MOONIDIH XV SEAM UG	8/2011	4/2015 (4/2022) [4/2022]	1,230.27 (-) [1,230.27]	414.42 (0.00) [84]
505	MURAI DIH UG TURN-KEY PROJECT	2/2011	4/2014 (-) [0/0]	339.88 (-) [339.88]	12.08 (0.00) [0]
506	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY)	2/2014	3/2021 (-) [3/2021]	555.52 (-) [555.52]	5.38 (0.00) [0]
507	NORTH URIMARI EXPANSION OCP	3/2019	3/2023 (-) [3/2023]	1,553.06 (-) [1,553.06]	204.04 (0.00) [0]
508	PATHERDIH NLW WASHERY	10/2012	4/2014 (-) [3/2020]	269.82 (-) [269.82]	181.30 (0.00) [71]
509	RAJRAPPA RCE OCP (3.0 MTY)	12/2009	3/2016 (-) [3/2021]	510.85 (-) [510.85]	399.09 (0.00) [60]
510	TAPIN OCP (2.5 MTY)	8/2008	3/2012 (-) [3/2021]	264.68 (-) [264.68]	181.17 (0.00) [108]
	Petroleum				
511	120 TMTPA NEW LPG PLANT AT BARHI JHARKAND STATE	6/2017	6/2020 (-) [9/2021]	161.50 (-) [161.50]	17.78 (0.00) [15]
512	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR	10/2017	10/2022 (-) [10/2022]	221.45 (-) [221.45]	52.67 (0.00) [0]
513	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI	10/2017	10/2022 (-) [10/2022]	226.45 (-) [226.45]	62.72 (0.00) [0]
514	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	12/2015	3/2023 (3/2022) [3/2022]	823.27 (910.23) [910.23]	441.81 (86.96) [-12]
515	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO.	11/2018	6/2022 (-) [6/2022]	248.55 (-) [248.55]	29.20 (0.00) [0]
	Power				
516	NORTH KARANPURA STPP (3X660 MW)	2/2014	6/2019 (9/2019) [3/2022]	14,366.58 (-) [15,164.05]	9,965.78 (797.47) [33]
517	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017 (-) [0/0]	4,237.96 (4,238.00) [4,552.00]	3,365.00 (314.04) [0]

518	PATRATU STPP-I (3X800MW)	11/2017	3/2023 (-) [3/2023]	18,668.00 (-) [18,668.00]	2,409.34 (0.00) [0]
	<u>Railways</u>				
519	BONDAMUNDA RANCHI DOUBLING	3/2016	3/2021 (3/2021) [12/2021]	1,724.20 (-) [1,993.24]	469.79 (269.04) [9]
520	GARHWA ROAD-RAMNA	3/2015	3/2021 (-) [12/2020]	348.23 (-) [348.23]	211.06 (0.00) [-3]
521	KODERMA-RANCHI VIA BARKAKANA (NL),ECR	3/1999	/ (-) [3/2021]	1,033.07 (3,020.95) [3,376.00]	3,349.65 (2,342.93) [-]
522	KODERMA-TILAIYA (NL), ECR	4/2002	/ (-) [3/2021]	459.91 (1,625.87) [1,625.87]	544.36 (1,165.96) [-]
523	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	4/2012	12/2018 (12/2018) [8/2020]	258.20 (358.68) [358.68]	278.34 (100.48) [20]
524	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	4/2012	12/2016 (8/2018) [3/2020]	148.77 (-) [377.00]	183.96 (228.23) [39]
	<u>Road Transport And Highways</u>				
525	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00)	3/2017	3/2020 (-) [3/2020]	239.68 (-) [235.90]	91.24 (-3.78) [0]
526	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00)	3/2017	3/2020 (-) [3/2020]	165.50 (-) [172.16]	117.09 (6.66) [0]
527	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K	3/2018	/ (3/2019) [3/2021]	1,005.08 (1,073.10) [1,005.08]	0.00 (0.00) [-]
528	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION	2/2016	3/2019 (-) [0/0]	997.15 (-) [997.15]	728.62 (0.00) [0]
529	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31	1/2018	/ (-) [0/0]	273.46 (-) [273.46]	0.00 (0.00) [0]
530	FOUR LANING OF BARHI-HAZARIBAGH NH-33	8/2016	8/2018 (-) [1/2020]	323.72 (-) [323.72]	232.58 (0.00) [17]
531	RANCHI-RARGA-JAMSETHPUR	12/2012	6/2015 (-) [0/0]	1,479.00 (-) [1,479.00]	740.26 (0.00) [0]
532	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L	3/2018	6/2020 (-) [6/2020]	212.99 (-) [212.99]	99.21 (0.00) [0]
533	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION	1/2018	/ (-) [0/0]	1,155.16 (-) [1,155.16]	30.13 (0.00) [0]
534	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH-	7/2016	/ (12/2017) [12/2019]	458.03 (-) [458.03]	338.86 (0.00) [0]
535	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I	12/2016	9/2021 (-) [9/2021]	196.00 (-) [196.00]	0.00 (0.00) [0]
	<u>Steel</u>				
536	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	5/2015	12/2017 (1/2020) [3/2020]	1,154.18 (-) [1,154.18]	998.53 (0.00) [27]
537	NEW SINTER PLANT AT BOKARO STEEL PLANT	3/2015	10/2017	1,034.01	450.11

			(6/2020) [6/2020]	(-) [1,034.01]	(0.00) [32]
538	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	11/2016	6/2019 (6/2020) [11/2020]	262.87 (-) [262.87]	131.30 (0.00) [17]
	<u>Urban Development</u>				
539	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	9/2012	3/2016 (-) [9/2020]	171.86 (-) [171.86]	97.70 (0.00) [54]
540	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT	12/2007	3/2018 (-) [0/0]	200.00 (-) [200.00]	131.15 (0.00) [0]
541	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY	4/2013	4/2018 (-) [0/0]	170.00 (-) [170.00]	88.91 (0.00) [0]
542	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII	2/2014	12/2016 (-) [0/0]	787.29 (-) [787.29]	285.30 (0.00) [0]
543	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY-JHARKHAND	12/2007	6/2016 (-) [0/0]	253.92 (253.92) [253.92]	193.97 (0.00) [0]
	<u>KARNATAKA</u>				
	<u>Petroleum</u>				
544	BSVI UPGRADATION	9/2016	12/2019 (7/2020) [3/2021]	1,810.00 (1,810.00) [1,810.00]	1,022.88 (0.00) [15]
545	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU	5/2015	4/2019 (-) [0/0]	224.00 (207.00) [185.00]	164.61 (-39.00) [0]
546	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE	12/2018	12/2022 (-) [12/2022]	854.00 (-) [854.00]	56.18 (0.00) [0]
547	GAIL GAS LTD BENGALURU CGD PROJECT	2/2015	2/2020 (-) [2/2020]	749.00 (-) [842.00]	606.89 (93.00) [0]
548	HASSAN CHERLAPALLI LPG PIPELINE	6/2019	6/2022 (-) [6/2022]	2,166.38 (-) [2,166.38]	33.41 (0.00) [0]
549	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE	10/2015	3/2019 (-) [0/0]	135.00 (171.00) [170.70]	156.65 (35.70) [0]
550	RESITEMENT OF RAICHUR DEPOT TO GULBARGA	10/2018	3/2021 (-) [3/2021]	206.26 (-) [206.26]	13.42 (0.00) [0]
551	SEA WATER DESALINATION PLANT	11/2017	3/2020 (11/2020) [11/2020]	581.00 (-) [621.00]	154.66 (40.00) [8]
552	SETTING UP OF PHASE LL FACILITIES FOR HPCL GREEN R AND D CENTRE AT BENGALURU	6/2018	11/2021 (-) [11/2021]	380.00 (-) [380.00]	82.70 (0.00) [0]
553	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	1/2006	1/2012 (-) [0/0]	993.00 (-) [1,693.00]	1,549.85 (700.00) [0]
	<u>Power</u>				
554	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B)	5/2017	2/2019 (12/2019) [5/2020]	445.89 (-) [445.89]	332.46 (0.00) [15]
	<u>Railways</u>				
555	ARSIKERE-TUMKUR	3/2015	3/2020 (-) [3/2020]	578.00 (578.00) [578.00]	565.04 (0.00) [0]

556	BAGALKOT-KUDACHI NL	4/2010	3/2016 (-) [12/2023]	986.30 (986.30) [986.30]	303.05 (0.00) [93]
557	BANGLORE - SATYAMANGALAM (NL)(SWR)	4/1996	3/2002 (-) [3/2024]	1,382.78 (1,382.78) [1,382.78]	7.35 (0.00) [264]
558	CHIKBALLA-PUR-GOWRIBIDANUR NL	4/2013	/ (-) [12/2023]	327.25 (367.77) [367.77]	0.00 (40.52) [-]
559	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	4/2013	/ (-) [12/2023]	558.00 (692.43) [692.43]	0.00 (134.43) [-]
560	GADAG-WADI NL	4/2013	12/2018 (-) [12/2024]	2,841.84 (2,841.84) [2,841.84]	194.25 (0.00) [72]
561	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	4/2010	3/2023 (-) [3/2024]	2,127.00 (-) [2,900.00]	1,815.11 (773.00) [12]
562	HUBLI- CHIKJAJUR	3/2015	3/2020 (-) [3/2021]	1,156.94 (1,140.94) [1,140.94]	918.47 (-16.00) [12]
563	HUBLI-ANKOLA(NL),SWR	4/1997	/ (-) [12/2024]	2,315.00 (-) [2,315.00]	151.40 (0.00) [-]
564	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	3/1996	3/2017 (-) [3/2020]	644.78 (644.78) [890.00]	461.80 (245.22) [36]
565	MARIKUPPAM - KUPPAM	4/2012	3/2016 (-) [12/2023]	279.54 (279.54) [279.54]	30.62 (0.00) [93]
566	SHIMOGA-HARIHAR NL	4/2011	3/2016 (-) [3/2024]	832.47 (832.47) [832.47]	0.94 (0.00) [96]
567	TORANAGALLU-RANJITPURA DL	4/2011	/ (-) [12/2023]	146.75 (146.75) [167.50]	0.34 (20.75) [-]
568	TUMKUR-CHITRADURGA-DAVENGERE NL	4/2011	/ (-) [12/2023]	1,801.01 (1,801.01) [1,801.01]	57.70 (0.00) [-]
569	WHITE FIELD-KOLAR NL	4/2011	/ (-) [12/2023]	348.85 (348.85) [348.85]	0.36 (0.00) [-]
<u>Road Transport And Highways</u>					
570	HOSPET-BELLARY-KARNATAKA AP BORDER	8/2016	3/2019 (3/2017) [8/2020]	1,167.42 (870.00) [870.00]	265.48 (-297.42) [17]
571	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM	2/2018	/ (-) [0/0]	486.78 (-) [486.78]	144.22 (0.00) [0]
572	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	5/2014	8/2016 (-) [12/2020]	1,655.01 (-) [1,655.01]	1,867.51 (0.00) [52]
573	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	3/2016	3/2019 (-) [11/2020]	701.40 (-) [701.40]	29.48 (0.00) [20]
574	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL	3/2016	3/2019 (-) [11/2020]	870.00 (-) [870.00]	36.30 (0.00) [20]
575	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION	2/2017	5/2019 (-) [5/2021]	157.32 (188.00) [157.32]	0.00 (0.00) [24]

576	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT	5/2018	5/2018 (-) [5/2020]	171.60 (-) [171.60]	0.86 (0.00) [24]
577	FOUR LANING OF HOSPET - CHITRADURGA	3/2015	8/2018 (-) [3/2020]	1,388.00 (-) [1,388.00]	1,203.00 (0.00) [19]
578	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB	8/2016	4/2020 (-) [4/2020]	1,664.20 (-) [1,664.20]	794.87 (0.00) [0]
579	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	9/2010	6/2018 (-) [12/2019]	946.00 (-) [946.00]	818.53 (0.00) [0]
580	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN	3/2018	10/2018 (-) [0/0]	325.86 (-) [325.86]	62.54 (0.00) [0]
581	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH	8/2016	2/2017 (-) [0/0]	175.50 (-) [175.50]	86.54 (0.00) [0]
582	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2	3/2018	6/2019 (-) [0/0]	159.97 (-) [159.97]	0.00 (0.00) [0]
583	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM.	1/2014	8/2014 (-) [0/0]	471.16 (-) [471.16]	128.32 (0.00) [0]
584	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	1/1991	1/2018 (-) [0/0]	219.40 (-) [219.40]	0.00 (0.00) [0]
585	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O	3/2017	3/2020 (-) [6/2020]	993.16 (-) [1,434.00]	765.31 (440.84) [3]
586	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	3/2017	3/2020 (-) [7/2020]	831.58 (-) [1,177.00]	702.31 (345.42) [4]
587	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA	2/2018	/ (10/2019) [0/0]	2,177.80 (2,283.50) [2,450.00]	931.86 (272.20) [0]
588	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT	2/2018	/ (5/2019) [11/2021]	1,995.34 (2,190.00) [2,400.00]	1,740.36 (404.66) [-]
589	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP	3/2015	11/2015 (-) [0/0]	165.67 (-) [165.67]	0.00 (0.00) [0]
590	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU	3/2015	11/2015 (-) [0/0]	159.12 (-) [159.12]	0.00 (0.00) [0]
591	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	9/2016	8/2019 (-) [12/2020]	950.69 (1,008.00) [1,108.00]	1,399.33 (157.31) [16]
592	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN	10/2016	3/2017 (-) [0/0]	396.96 (-) [396.96]	113.98 (0.00) [0]
593	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT	11/2016	3/2017 (-) [0/0]	314.90 (-) [314.90]	104.40 (0.00) [0]
594	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT	8/2016	1/2017 (-) [0/0]	367.44 (-) [367.44]	61.95 (0.00) [0]
595	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT	8/2016	2/2017 (-) [0/0]	329.01 (-) [329.01]	135.50 (0.00) [0]
596	WIDENING TO TWO LANE WITH PAVED SHOULDER	9/2017	10/2018	191.60	26.24

	FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR		(-) [0/0]	(-) [191.60]	(0.00) [0]
597	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U	1/2017	8/2017 (-) [0/0]	291.49 (-) [291.49]	130.00 (0.00) [0]
598	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA	1/2017	9/2017 (-) [0/0]	166.67 (-) [166.67]	117.05 (0.00) [0]
599	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT	8/2016	1/2017 (-) [0/0]	175.20 (-) [175.20]	113.38 (0.00) [0]
600	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH-	12/2017	1/2019 (-) [0/0]	297.30 (-) [297.30]	0.00 (0.00) [0]
601	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION	1/2018	7/2018 (-) [0/0]	159.70 (-) [159.70]	22.79 (0.00) [0]
602	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776)	3/2015	1/2016 (-) [0/0]	165.67 (-) [165.67]	87.63 (0.00) [0]
603	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775)	3/2015	1/2016 (-) [0/0]	159.12 (-) [159.12]	96.22 (0.00) [0]
	<u>Urban Development</u>				
604	BANGALORE METRO RAIL PROJECT PHASE-2	2/2014	2/2019 (-) [3/2020]	26,405.14 (-) [26,405.14]	499.85 (0.00) [13]
605	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	5/2005	2/2014 (-) [0/0]	768.88 (1,070.97) [1,113.34]	1,085.64 (344.46) [0]
606	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA	7/2011	12/2015 (-) [0/0]	324.87 (324.87) [324.87]	262.93 (0.00) [0]
607	RESIDENTIAL QUATERS FOR HAL,BANGLORE	12/2016	2/2020 (-) [9/2020]	246.31 (-) [246.31]	85.43 (0.00) [7]
	<u>KERALA</u>				
	<u>Petroleum</u>				
608	KOCHI SALEM LPG PIPELINE PROJECT	12/2015	6/2019 (2/2022) [2/2022]	1,112.00 (1,507.24) [1,507.24]	566.00 (395.24) [32]
609	LPG TERMINAL AT KOCHI	10/2015	10/2017 (-) [0/0]	607.06 (-) [714.25]	356.62 (107.19) [0]
610	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY	2/2016	2/2020 (10/2020) [10/2020]	3,313.00 (3,288.96) [3,288.96]	1,673.55 (-24.04) [8]
611	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	11/2014	8/2018 (11/2019) [2/2020]	4,588.29 (5,245.96) [5,245.96]	4,137.20 (657.67) [18]
612	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC	9/2018	3/2023 (-) [3/2023]	11,130.00 (-) [11,130.00]	89.09 (0.00) [0]
	<u>Railways</u>				
613	ANGAMALI-SABARIMALA (N.L.)(SR)	10/1998	/	1,566.00	264.28
			(-) [0/0]	(-) [2,815.62]	(1,249.62) [0]
614	ERNAKULAM-KUMBALAM	4/2010	/	189.24	6.72
			(-) [0/0]	(-) [189.24]	(0.00) [0]
615	KUMBALAM-TURAVUR	4/2011	/	252.96	8.50

			(-) [0/0]	(-) [252.96]	(0.00) [0]
616	PALAKKAD - SETTING UP OF RAIL COACH FACTORY	2/2012	3/2016 (-) [0/0]	550.00 (-) [550.00]	0.00 (0.00) [0]
617	TRIVANDRUM-KANYAKUMARI DOUBLING	2/2015	/ (-) [0/0]	1,431.90 (-) [1,431.90]	75.00 (0.00) [0]
618	TURAVUR-AMBALAPUZHA DOUBLING	2/2015	/ (-) [0/0]	1,000.00 (-) [828.50]	0.08 (-171.50) [0]
Road Transport And Highways					
619	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47	6/2015	/ (-) [1/2020]	845.24 (-) [941.00]	859.59 (95.76) [-]
620	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T	4/2016	6/2018 (-) [3/2020]	804.97 (-) [804.97]	465.05 (0.00) [21]
621	4-LANNING OF THALSERRY -MAHE BYPASS	9/2017	9/2017 (-) [5/2021]	1,124.11 (-) [1,232.76]	314.14 (108.65) [44]
622	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH	2/2018	/ (-) [0/0]	1,424.77 (-) [1,853.42]	14.19 (428.65) [0]
623	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1	1/2014	9/2017 (-) [0/0]	255.75 (348.00) [348.43]	290.12 (92.68) [0]
624	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM	2/2010	8/2012 (-) [12/2019]	617.00 (-) [617.00]	943.17 (0.00) [0]
Urban Development					
625	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST)	9/2017	3/2020 (11/2020) [3/2021]	150.29 (-) [150.29]	21.82 (0.00) [12]
626	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	1/2010	10/2012 (-) [3/2020]	165.23 (-) [165.23]	100.81 (0.00) [89]
627	KOCHI METRO RAIL PROJECT	7/2012	7/2017 (-) [3/2020]	5,181.79 (5,687.79) [6,218.14]	5,817.11 (1,036.35) [32]
MADHYA PRADESH					
Coal					
628	AMADAND OPENCASE EXPANSION PROJECT	3/2016	3/2021 (-) [3/2021]	869.44 (-) [869.44]	117.99 (0.00) [0]
629	AMRITDHARA OC PROJECT	2/2015	3/2023 (-) [3/2023]	481.60 (-) [481.60]	0.00 (0.00) [0]
630	BATURA HIGHWALL PROJECT	7/2015	3/2022 (-) [3/2022]	231.92 (-) [231.92]	0.00 (0.00) [0]
631	BLOCK-B EXPANSION OPENCASE PROJECT	7/2019	3/2023 (-) [3/2023]	998.71 (-) [998.71]	0.00 (0.00) [0]
632	COAL PROJECT NAME JAMUNIA UG (0.84 MTY)	7/2016	3/2022 (-) [3/2022]	409.87 (-) [409.87]	19.96 (0.00) [0]
633	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA)	11/2017	3/2022 (-) [3/2022]	1,255.17 (-) [1,255.17]	123.08 (0.00) [0]
634	GANDHIGRAM UG MINE	8/2019	3/2026	414.16	0.50

			(-) [3/2026]	(-) [414.16]	(0.00) [0]
635	JAYANT EXPANSION OCP 10 TO 20 MTPA	5/2017	3/2021 (-) [3/2021]	1,783.09 (-) [1,783.09]	292.75 (0.00) [0]
636	KANCHAN OC EXPANSION	12/2014	3/2021 (-) [3/2021]	371.04 (-) [371.04]	48.13 (0.00) [0]
637	MALACHUA OPENCAST PROJECT	10/2015	3/2023 (-) [3/2023]	488.33 (-) [488.33]	27.33 (0.00) [0]
638	RAJNAGAR OCP RPR (1.70 MTY)	12/2014	3/2021 (-) [3/2021]	357.80 (-) [357.80]	104.77 (0.00) [0]
639	SEMARIA OPENCAST PROJECT	5/2019	3/2026 (-) [3/2026]	396.58 (-) [396.58]	0.00 (0.00) [0]
640	VISHNUPURI UG TO OC MINE	7/2018	3/2025 (-) [3/2025]	195.57 (-) [195.57]	2.94 (0.00) [0]
	<u>Petroleum</u>				
641	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND	8/2017	6/2020 (-) [10/2020]	236.00 (-) [236.00]	49.62 (0.00) [4]
	<u>Power</u>				
642	AMELIA COAL MINE	1/2017	9/2020 (-) [9/2020]	2,104.21 (-) [1,587.16]	309.90 (-517.05) [0]
643	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	3/2013	1/2018 (3/2020) [3/2020]	11,638.55 (-) [12,865.92]	12,503.29 (1,227.37) [26]
644	KHARGONE STPP STAGE I (1320 MW)	3/2015	1/2020 (-) [2/2020]	9,870.51 (-) [11,148.86]	9,430.15 (1,278.35) [1]
	<u>Railways</u>				
645	ANUPPUR-KATNI	4/2015	12/2021 (3/2023) [3/2023]	1,370.00 (1,370.94) [1,370.94]	332.76 (0.94) [15]
646	BINA - KOTA DOUBLING WITH RE	4/2011	12/2020 (-) [3/2021]	1,485.85 (-) [1,485.85]	1,196.74 (0.00) [3]
647	CHHINDWARA - NAGPUR (GC)(SECR)	4/2005	/ (1/2020) [1/2020]	383.79 (1,473.76) [1,413.76]	1,351.73 (1,029.97) [-]
648	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	4/2010	2/2019 (12/2020) [12/2020]	585.93 (1,268.32) [1,268.32]	687.95 (682.39) [22]
649	INDORE-DEWAS-UJJAIN (80 KMS)	4/2016	6/2020 (6/2021) [6/2021]	700.00 (603.69) [603.69]	146.09 (-96.31) [12]
650	KATNI - SINGRAULI DOUBLING PROJECT	12/2015	3/2020 (-) [3/2023]	1,763.93 (-) [1,762.94]	867.52 (-0.99) [36]
651	KATNI GRADE SEPARATOR/BYE PASS	8/2016	3/2022 (-) [9/2022]	582.13 (-) [1,247.64]	228.36 (665.51) [6]
652	KATNI-BINA 3RD LINE (263 KM)	6/2016	3/2022 (-) [3/2023]	2,478.23 (-) [2,478.23]	477.93 (0.00) [12]
653	MULTI MODAL LOGISTICS PARK AT TIHI	12/2015	3/2019 (-)	174.00 (-)	164.41 (0.00)

			[2/2020]	[174.00]	[11]
654	RAMGANJMUNDI-BHOPAL (NL),WCR	4/2001	3/2021 (-) [3/2023]	424.60 (-) [2,909.99]	1,975.34 (2,485.39) [24]
655	RATLAM-MHOW-KHANDWA-AKOLA (GC)	4/2008	3/2022 (3/2023) [3/2023]	3,503.69 (3,975.22) [3,975.22]	1,801.98 (471.53) [12]
	Road Transport And Highways				
656	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP	3/2018	11/2019 (-) [5/2020]	191.21 (-) [191.21]	78.35 (0.00) [6]
657	2L+PS OF THIKRI ANJAD SECTION OF NH-347B	11/2017	7/2018 (-) [6/2020]	249.05 (-) [249.05]	143.64 (0.00) [23]
658	ANJANGAON TO MAH/MP BORDER	1/2017	6/2019 (-) [0/0]	359.00 (359.00) [359.00]	221.80 (0.00) [0]
659	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN	12/2017	/ (-) [0/0]	950.27 (-) [950.27]	168.05 (0.00) [0]
660	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM.	11/2017	3/2018 (-) [9/2020]	392.33 (428.55) [428.55]	253.99 (36.22) [30]
661	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION	8/2016	1/2019 (-) [12/2019]	227.49 (-) [227.49]	129.93 (0.00) [0]
662	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12	9/2017	9/2017 (-) [0/0]	374.40 (-) [204.65]	155.83 (-169.75) [0]
663	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69	9/2017	9/2017 (-) [1/2021]	990.61 (-) [990.61]	397.89 (0.00) [40]
664	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP	8/2015	/ (-) [0/0]	257.80 (-) [257.00]	12.38 (-0.80) [0]
665	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A	6/2015	/ (-) [3/2020]	390.51 (-) [390.51]	209.67 (0.00) [-]
666	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V	12/2017	/ (-) [0/0]	656.98 (-) [656.98]	2.48 (0.00) [0]
667	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA	10/2019	/ (-) [0/0]	743.88 (-) [743.88]	0.00 (0.00) [0]
668	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA	12/2017	/ (-) [0/0]	1,094.97 (-) [1,094.97]	1.51 (0.00) [0]
669	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM	12/2017	/ (-) [0/0]	217.96 (-) [217.96]	0.50 (0.00) [0]
670	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH.	1/2017	3/2017 (-) [9/2020]	205.05 (-) [205.05]	85.57 (0.00) [42]
671	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD	1/2019	3/2021 (-) [3/2021]	264.50 (-) [264.50]	0.00 (0.00) [0]
672	FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR	6/2015	1/2019 (10/2019) [10/2019]	1,583.79 (-) [1,583.79]	1,648.90 (0.00) [0]
673	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM	1/2018	/ (-)	960.24 (-)	328.34 (0.00)

	624.480 TO		[0/0]	[960.24]	[0]
674	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA	6/2015	3/2016 (-) [0/0]	1,012.90 (-) [1,012.90]	226.10 (0.00) [0]
675	FOUR LANING OF GWALIOR-SHIVPURI	5/2013	11/2015 (-) [0/0]	1,055.00 (-) [1,601.77]	1,393.40 (546.77) [0]
676	FOUR LANING OF JABALPUR - LAKHNADON	3/2015	/ (6/2015) [6/2015]	928.83 (-) [928.83]	709.38 (0.00) [0]
677	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I	3/2015	/ (-) [12/2019]	794.30 (637.86) [691.38]	637.86 (-102.92) [0]
678	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II	3/2015	/ (-) [3/2020]	795.76 (659.57) [677.72]	659.57 (-118.04) [-]
679	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV	3/2015	/ (6/2015) [6/2015]	810.22 (-) [810.22]	721.55 (0.00) [0]
680	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124.	10/2017	10/2017 (-) [1/2020]	639.97 (-) [639.97]	331.84 (0.00) [27]
681	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER	1/2018	/ (-) [0/0]	770.73 (-) [770.73]	59.45 (0.00) [0]
682	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93	12/2015	2/2020 (-) [8/2020]	957.54 (-) [957.54]	573.28 (0.00) [6]
683	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	11/2013	5/2017 (-) [5/2020]	497.05 (-) [881.05]	624.54 (384.00) [36]
684	INDORE-DEWAS(NH-3)	11/2010	5/2013 (-) [0/0]	325.00 (-) [475.00]	469.54 (150.00) [0]
685	INDORE-JHABUA-GUJRAT/MP	10/2010	4/2013 (-) [0/0]	1,175.00 (-) [1,175.00]	1,509.96 (0.00) [0]
686	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400	11/2015	1/2020 (-) [9/2020]	628.45 (-) [628.45]	300.52 (0.00) [8]
687	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP	1/2012	4/2015 (-) [10/2019]	410.72 (-) [410.72]	390.00 (0.00) [0]
688	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA	2/2018	3/2018 (-) [7/2020]	169.63 (-) [169.63]	14.67 (0.00) [28]
689	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86	9/2016	9/2018 (-) [8/2019]	178.23 (-) [178.23]	122.99 (0.00) [0]
690	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175	9/2016	1/2019 (-) [3/2020]	287.34 (-) [287.34]	158.05 (0.00) [14]
691	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM	3/2016	6/2019 (-) [7/2020]	877.79 (-) [877.79]	467.48 (0.00) [13]
692	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID	11/2017	2/2018 (-) [5/2020]	235.91 (-) [235.91]	156.89 (0.00) [27]
693	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS	1/2016	7/2018 (-) [9/2020]	809.16 (-) [809.16]	353.90 (0.00) [26]

694	SATANA-BELA SECTION OF NH-75(4L) IN MP	1/2012	8/2015 (-) [0/0]	320.48 (-) [320.48]	189.49 (0.00) [0]
695	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	11/2011	9/2015 (-) [10/2021]	954.43 (1,191.51) [1,191.51]	235.61 (237.08) [73]
696	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200	3/2015	8/2017 (-) [2/2020]	511.83 (-) [511.83]	278.88 (0.00) [30]
697	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS	11/2017	2/2018 (-) [9/2020]	254.17 (-) [254.17]	157.83 (0.00) [31]
698	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS	3/2018	3/2018 (-) [4/2020]	233.04 (-) [233.04]	131.22 (0.00) [25]
699	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS	2/2018	3/2018 (-) [4/2020]	279.44 (-) [279.44]	76.00 (0.00) [25]
700	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS	3/2018	8/2018 (-) [6/2020]	166.21 (-) [166.21]	67.45 (0.00) [22]
701	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS	11/2017	2/2018 (-) [5/2020]	184.62 (-) [184.62]	76.60 (0.00) [27]
702	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS	3/2018	3/2018 (-) [12/2020]	214.69 (-) [214.69]	30.44 (0.00) [33]
703	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS	3/2018	8/2018 (-) [6/2020]	217.22 (226.88) [226.88]	86.83 (9.66) [22]
704	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS	3/2018	3/2018 (-) [5/2020]	162.56 (-) [162.56]	119.50 (0.00) [26]
705	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A	1/2017	9/2019 (-) [9/2020]	373.82 (-) [373.82]	143.05 (0.00) [12]
	<u>Urban Development</u>				
706	BHOPAL METRO RAIL	11/2018	2/2023 (-) [2/2023]	6,941.40 (-) [6,941.40]	58.37 (0.00) [0]
707	INDORE METRO RAIL	11/2018	2/2023 (-) [2/2023]	7,500.80 (-) [7,500.80]	54.74 (0.00) [0]
	<u>MAHARASHTRA</u>				
	<u>Civil Aviation</u>				
708	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT	3/2017	4/2021 (-) [4/2021]	358.89 (-) [358.89]	29.73 (0.00) [0]
	<u>Coal</u>				
709	ADASA UG TO OC	8/2015	3/2023 (-) [3/2024]	288.90 (-) [333.43]	38.82 (44.53) [12]
710	AMALGAMATED GONDEGAON GHATROHAN OC	2/2016	3/2019 (-) [0/0]	198.68 (-) [198.68]	190.04 (0.00) [0]
711	AMALGAMATED PAUNI-II III OC MINE	6/2015	3/2021 (-) [3/2021]	483.69 (-) [483.69]	225.02 (0.00) [0]
712	AMALGAMATED YEKONA-I YEKONA-II	8/2015	3/2025 (-) [3/2025]	727.28 (-) [727.28]	263.81 (0.00) [0]

713	BELLORA-NAIGAON DEEP OC	11/2018	3/2021 (-) [3/2021]	252.71 (-) [252.71]	58.07 (0.00) [0]
714	BHANEGAON OC	2/2015	3/2023 (-) [3/2023]	187.94 (-) [409.68]	129.61 (221.74) [0]
715	BHATADI EXPANSION OC MINE	2/2016	3/2019 (-) [0/0]	304.52 (-) [304.52]	155.34 (0.00) [0]
716	DINESH OCP	11/2014	3/2020 (-) [3/2020]	611.16 (-) [611.16]	415.50 (0.00) [0]
717	GAURI DEEP OC	10/2016	3/2019 (-) [0/0]	164.96 (-) [164.96]	95.86 (0.00) [0]
718	KAMPTEE DEEP OC MINE	11/2015	3/2021 (-) [3/2024]	277.65 (-) [313.34]	118.18 (35.69) [36]
719	KOLAR PIMPRI EXTENSION OC	3/2017	3/2020 (-) [3/2020]	362.73 (-) [362.73]	322.62 (0.00) [0]
720	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE	11/2015	3/2020 (-) [3/2020]	498.42 (-) [498.42]	202.03 (0.00) [0]
721	NEW MAJRI UG TO OC	5/2015	3/2019 (-) [0/0]	295.56 (-) [295.56]	121.46 (0.00) [0]
722	PENGANGA OCP(REVISED)	9/2014	3/2020 (-) [3/2020]	441.82 (-) [441.82]	218.63 (0.00) [0]
723	SAONER I UG TO OC PHASE I	11/2016	3/2022 (-) [3/2022]	162.10 (-) [162.10]	51.16 (0.00) [0]
724	SINGHORI OC MINE	6/2015	3/2020 (-) [3/2020]	205.49 (-) [205.49]	120.69 (0.00) [0]
725	UKNI DEEP OC	11/2018	3/2021 (-) [3/2021]	318.14 (-) [318.14]	148.14 (0.00) [0]
	<u>Fertilisers</u>				
726	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY	4/2018	4/2020 (7/2020) [4/2020]	426.72 (-) [426.72]	268.46 (0.00) [0]
	<u>Health And Family Welfare</u>				
727	HOSPITAL AND TEACHING- AIIMS NAGPUR	3/2018	/ (-) [6/2020]	582.99 (-) [582.99]	268.43 (0.00) [-]
728	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA	8/2017	3/2019 (-) [3/2020]	274.19 (-) [274.19]	230.83 (0.00) [12]
	<u>Petroleum</u>				
729	180 TMTPA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA	6/2017	6/2020 (-) [9/2021]	249.26 (-) [249.26]	62.55 (0.00) [15]
730	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELI	5/2016	1/2021 (-) [1/2021]	261.00 (-) [261.00]	71.13 (0.00) [0]
731	ADDITIONAL FACILITIES AT MANMAD FOR COVERION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [4/2021]	212.00 (-) [212.00]	57.97 (0.00) [3]
732	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION	5/2016	1/2021	348.00	101.41

	TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE		(-) [10/2021]	(-) [348.00]	(0.00) [9]
733	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	3/2011	5/2013 (2/2020) [2/2020]	861.79 (-) [1,683.06]	1,386.15 (821.27) [81]
734	DEVELOPMENT OF B-147 FIELD	2/2017	11/2019 (3/2020) [3/2020]	546.15 (565.15) [565.15]	468.71 (19.00) [4]
735	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION	2/2019	5/2021 (-) [5/2021]	2,292.46 (-) [2,292.46]	815.60 (0.00) [0]
736	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)	2/2017	5/2021 (12/2021) [12/2021]	4,006.83 (-) [4,475.92]	2,975.26 (469.09) [7]
737	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA	1/2015	12/2017 (3/2020) [3/2020]	4,619.94 (-) [4,619.94]	4,586.11 (0.00) [27]
738	HEERA REDEVELOPMENT - PHASE III	5/2019	12/2021 (-) [3/2022]	2,494.68 (-) [2,494.68]	270.26 (0.00) [3]
739	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY	2/2016	2/2020 (-) [2/2020]	554.00 (-) [554.00]	375.80 (0.00) [0]
740	INTEGRATED DEVELOPMENT OF B-127 FIELDS	12/2011	3/2015 (3/2020) [3/2020]	2,059.63 (2,665.65) [2,665.65]	1,933.09 (606.02) [60]
741	KOYALI AHMEDNAGAR SOLAPUR PIPELINE	5/2016	8/2021 (-) [8/2021]	1,945.00 (-) [1,945.00]	1,074.02 (0.00) [0]
742	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	12/2015	4/2018 (5/2020) [5/2020]	3,190.69 (-) [3,247.19]	2,369.08 (56.50) [25]
743	MMPL PIPELINE REROUTING PROJECT	4/2013	12/2019 (7/2020) [7/2020]	449.58 (-) [449.58]	215.10 (0.00) [7]
744	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	4/2019	3/2022 (-) [3/2022]	3,228.80 (-) [3,228.80]	510.66 (0.00) [0]
745	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III	11/2014	4/2019 (3/2020) [3/2020]	6,068.80 (-) [5,296.93]	4,845.91 (-771.87) [11]
746	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV	2/2019	4/2021 (-) [5/2021]	3,660.71 (3,740.05) [3,740.05]	373.79 (79.34) [1]
747	MUMBAI REFINERY EXPANSION PROJECT	9/2015	3/2020 (-) [3/2020]	4,199.00 (5,060.00) [5,060.00]	3,446.40 (861.00) [0]
748	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY	8/2015	3/2019 (5/2020) [5/2020]	2,818.88 (-) [2,818.88]	2,401.67 (0.00) [14]
749	PIPELINE REPLACEMENT PROJECT (PRP-VI)	5/2019	12/2020 (-) [12/2020]	763.92 (-) [763.92]	205.99 (0.00) [0]
750	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE)	4/2018	12/2019 (3/2020) [3/2020]	766.37 (-) [766.37]	481.94 (0.00) [3]
751	PUNE POL STORAGE DEPOT	8/2016	8/2020 (-) [8/2020]	282.64 (-) [282.64]	164.77 (0.00) [0]
	<u>Power</u>				
752	MOUDA STPP STAGE 2	3/2012	9/2016	7,921.47	5,302.00

			(-) [0/0]	(-) [7,921.47]	(0.00) [0]
	Railways				
753	3RD LINE BETWEEN BHUSAWAL-JALGAON	4/2011	3/2019 (3/2020) [3/2020]	184.06 (199.12) [312.00]	293.06 (127.94) [12]
754	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	2/1997	3/2021 (-) [3/2022]	2,271.50 (-) [4,517.49]	2,495.07 (2,245.99) [12]
755	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	3/1996	3/2004 (-) [3/2021]	495.44 (1,781.98) [2,980.41]	1,457.78 (2,484.97) [204]
756	DAUND - MANMAD (236 KM)	2/2016	3/2023 (-) [3/2023]	1,876.00 (-) [2,081.27]	230.40 (205.27) [0]
757	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	3/2009	3/2020 (-) [3/2021]	713.48 (-) [2,300.00]	2,131.56 (1,586.52) [12]
758	DIGHI PORT NEW LINE	4/2015	12/2025 (-) [3/2025]	723.78 (-) [723.78]	0.19 (0.00) [-9]
759	INDORE - MANMAD VIA MALEGAON (368 KM)	2/2016	3/2024 (-) [3/2024]	9,968.00 (-) [9,968.00]	0.00 (0.00) [0]
760	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	2/2015	3/2023 (-) [3/2023]	2,449.91 (-) [2,449.91]	218.30 (0.00) [0]
761	KALYAN-KASARA 3RD LINE	4/2011	3/2021 (-) [3/2022]	792.89 (-) [1,377.48]	318.59 (584.59) [12]
762	MANMAD - JALGAON - 3RD LINE (160 KM)	2/2016	3/2022 (-) [3/2024]	1,035.16 (-) [1,035.16]	138.46 (0.00) [24]
763	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN	10/2013	3/2019 (-) [12/2019]	305.00 (-) [305.00]	261.83 (0.00) [0]
764	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM	3/2010	/ (-) [0/0]	265.88 (-) [265.88]	0.00 (0.00) [0]
765	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	4/2008	3/2014 (-) [3/2021]	5,300.00 (-) [918.53]	284.75 (-4,381.47) [84]
766	PUNE-MIRAJ-LONDA (467 KM)	2/2015	3/2024 (-) [3/2023]	3,627.47 (3,627.00) [3,627.47]	854.93 (0.00) [-12]
767	PUNE-NASIK (265 KM)	2/2016	3/2024 (-) [3/2024]	2,425.00 (-) [5,341.68]	0.00 (2,916.68) [0]
768	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	9/2016	3/2023 (3/2023) [3/2023]	1,908.51 (2,686.63) [2,686.63]	540.55 (778.12) [0]
769	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE	4/2012	4/2016 (-) [0/0]	714.10 (-) [714.10]	65.20 (0.00) [0]
770	VAIBHAVWADI -KOLHAPUR (107 KM)	2/2016	3/2024 (-) [0/0]	2,750.00 (-) [3,438.51]	0.00 (688.51) [0]
771	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A	3/2012	/ (-) [0/0]	217.38 (-) [217.38]	0.00 (0.00) [0]
772	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	6/2018	12/2021	229.00	39.69

			(3/2023) [3/2023]	(852.50) [852.50]	(623.50) [15]
773	WARDHA - NAGPUR - 4TH LINE (76 KM)	2/2016	3/2023 (-) [3/2024]	637.95 (-) [637.95]	76.12 (0.00) [12]
774	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	2/2015	3/2022 (-) [3/2023]	1,272.19 (-) [1,272.19]	339.43 (0.00) [12]
775	WARDHA-NANDED MAHARASHTRA	4/2008	3/2023 (-) [3/2023]	3,168.29 (-) [3,168.29]	1,268.08 (0.00) [0]
776	WARDHA-SEWAGRAM NGP 3RD LINE	4/2012	3/2022 (-) [3/2024]	540.02 (-) [540.02]	265.90 (0.00) [24]
	Road Transport And Highways				
777	4 LANING OF AMRAVATI - CHIKHLI (PKG-I)	7/2015	5/2019 (-) [0/0]	2,288.18 (-) [2,288.18]	487.81 (0.00) [0]
778	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3)	7/2015	5/2019 (-) [0/0]	1,885.74 (-) [1,885.74]	1,636.02 (0.00) [0]
779	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	1/2015	7/2017 (12/2019) [3/2020]	972.50 (-) [972.50]	1,492.00 (0.00) [32]
780	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104)	1/2018	/ (2/2019) [8/2021]	607.00 (512.99) [607.00]	187.53 (0.00) [-]
781	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000)	1/2018	/ (10/2018) [4/2021]	621.00 (565.02) [621.00]	383.83 (0.00) [-]
782	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION	6/2014	11/2016 (-) [5/2020]	923.04 (-) [923.04]	767.17 (0.00) [42]
783	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	3/2017	3/2020 (-) [3/2020]	744.64 (-) [982.00]	0.00 (237.36) [0]
784	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700)	11/2016	/ (-) [7/2021]	1,071.61 (-) [1,048.10]	514.46 (-23.51) [-]
785	4-LANNING OF KODEBAD-DHANTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT	11/2016	3/2019 (-) [3/2021]	446.17 (-) [446.17]	38.97 (0.00) [24]
786	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575)	3/2017	3/2020 (-) [8/2020]	1,098.06 (-) [1,160.64]	1,068.76 (62.58) [5]
787	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE	3/2016	/ (-) [0/0]	1,142.62 (-) [1,142.62]	836.85 (0.00) [0]
788	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE	3/2016	/ (-) [0/0]	1,101.58 (-) [1,101.58]	315.00 (0.00) [0]
789	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI	11/2016	3/2019 (-) [2/2021]	400.25 (-) [400.25]	64.89 (0.00) [23]
790	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00)	11/2016	/ (-) [7/2021]	1,064.88 (-) [1,021.00]	124.00 (-43.88) [-]
791	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580)	3/2017	3/2017 (5/2018) [11/2020]	1,059.73 (-) [1,071.00]	610.87 (11.27) [44]
792	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500	3/2017	3/2020	1,030.44	1,015.76

	TO 524.690)		(-) [5/2020]	(-) [1,065.51]	(35.07) [2]
793	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500)	3/2017	3/2020 (-) [8/2020]	988.34 (988.00) [1,043.28]	1,035.00 (54.94) [5]
794	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3	8/2015	5/2018 (4/2019) [9/2020]	505.00 (-) [504.00]	241.74 (-1.00) [28]
795	AHMADPUR TO PIMPLA	1/2017	8/2019 (-) [8/2019]	422.38 (422.38) [422.38]	161.58 (0.00) [0]
796	AHMEDNAGAR TO BARAMATI	1/2017	8/2019 (-) [8/2019]	955.40 (-) [955.40]	385.50 (0.00) [0]
797	AKKALKOT TO DHUDHNI	4/2016	2/2019 (-) [2/2020]	211.42 (-) [211.42]	131.85 (0.00) [12]
798	AKOLA TO AKOT	1/2017	6/2019 (-) [0/0]	313.95 (-) [313.95]	48.24 (0.00) [0]
799	AKOT TO ANJANGAON	1/2017	6/2019 (-) [0/0]	245.77 (246.00) [245.77]	158.98 (0.00) [0]
800	AMDNI TO SAONER	1/2017	6/2019 (-) [8/2019]	396.91 (396.91) [396.91]	254.48 (0.00) [0]
801	ARDHAPUR TO HIMAYATNAGAR	12/2017	6/2020 (-) [6/2020]	426.06 (426.00) [426.06]	91.97 (0.00) [0]
802	ARNI TO NAIGAINBANDI	12/2017	12/2019 (-) [12/2019]	309.94 (310.00) [309.94]	71.32 (0.00) [0]
803	AURANGABAD TO SILLOD	2/2017	6/2019 (-) [0/0]	456.32 (-) [456.32]	116.75 (0.00) [0]
804	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62	3/2016	7/2018 (-) [0/0]	197.69 (151.11) [197.69]	151.11 (0.00) [0]
805	BAMNI TO NAVAEGAON	9/2017	4/2020 (-) [4/2020]	241.69 (242.00) [241.69]	109.29 (0.00) [0]
806	BARASGAON TO RAHATEE	7/2016	9/2018 (-) [4/2021]	289.11 (290.00) [289.11]	33.82 (0.00) [31]
807	BHADGAON TO CHALISGAON	1/2018	11/2019 (-) [11/2019]	259.55 (260.00) [259.55]	182.24 (0.00) [0]
808	BHANDARA TO GHOTITOK	1/2017	6/2019 (-) [0/0]	392.83 (393.00) [392.83]	286.60 (0.00) [0]
809	BHOGAN KHURD TO KASHEDI	9/2017	6/2021 (-) [6/2021]	743.21 (743.00) [743.21]	131.87 (0.00) [0]
810	BHOKAR TO SARSAM	2/2017	7/2019 (-) [0/0]	295.09 (-) [295.99]	179.64 (0.90) [0]
811	BODHWAD TO STATE BORDER	1/2017	7/2019 (-) [0/0]	178.26 (-) [178.26]	124.95 (0.00) [0]
812	CHALISGAON TO NANDGAON	3/2018	12/2019 (-)	206.97 (207.00)	94.89 (0.00)

			[12/2019]	[206.97]	[0]
813	CHIKALI TO DHAD	3/2018	12/2019 (-) [12/2019]	189.46 (189.00) [189.46]	35.54 (0.00) [0]
814	CHIKALI TO KHAMGAON	2/2017	6/2019 (-) [10/2019]	548.03 (548.00) [548.03]	319.00 (0.00) [0]
815	CHIKLI TO TAKARKHED	3/2018	12/2019 (-) [12/2019]	393.10 (393.10) [393.10]	166.97 (0.00) [0]
816	CHIMUR TO WARORA	11/2016	3/2019 (-) [0/0]	467.70 (-) [467.70]	156.72 (0.00) [0]
817	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF	3/2018	/ (-) [7/2021]	1,162.92 (-) [1,162.92]	15.36 (0.00) [-]
818	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	12/2015	3/2019 (4/2021) [4/2021]	649.50 (-) [649.50]	155.81 (0.00) [25]
819	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6)	3/2018	/ (11/2020) [11/2020]	291.53 (-) [291.53]	68.92 (0.00) [-]
820	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST	1/2017	5/2019 (-) [12/2019]	244.90 (-) [244.90]	251.87 (0.00) [0]
821	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6)	3/2018	/ (-) [11/2020]	289.21 (-) [289.21]	41.34 (0.00) [-]
822	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	10/2015	5/2018 (6/2020) [6/2020]	593.26 (41.54) [636.24]	490.35 (42.98) [25]
823	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION	12/2011	/ (-) [0/0]	156.26 (227.00) [247.95]	175.00 (91.69) [0]
824	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	10/2015	5/2018 (-) [9/2020]	531.13 (-) [727.00]	524.15 (195.87) [28]
825	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16)	3/2015	/ (-) [0/0]	168.30 (-) [168.30]	80.00 (0.00) [0]
826	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO	8/2014	7/2016 (-) [0/0]	187.79 (-) [187.79]	76.62 (0.00) [0]
827	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST	3/2017	3/2020 (2/2021) [2/2020]	247.02 (-) [157.49]	31.97 (-89.53) [-1]
828	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D	9/2015	5/2018 (5/2020) [5/2020]	414.51 (414.00) [414.00]	543.46 (-0.51) [24]
829	DAHEGAON TO KUHI	1/2017	6/2019 (-) [0/0]	228.89 (229.00) [228.89]	130.00 (0.00) [0]
830	DASTAPUR TO KARANJA	3/2018	12/2019 (-) [12/2019]	182.63 (-) [182.63]	114.40 (0.00) [0]
831	DEORI TO AMGAON	1/2017	5/2019 (-) [5/2020]	409.62 (410.00) [409.62]	181.78 (0.00) [12]
832	DEULGAON SAKARSHA TO MEHKAR	3/2018	12/2019 (-) [12/2019]	219.91 (-) [219.91]	123.76 (0.00) [0]

833	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000)	3/2017	3/2020 (-) [3/2020]	296.19 (-) [254.00]	254.85 (-42.19) [0]
834	DHAD BHOKARDAN TO BHOKARDHAN SILLOD	3/2018	12/2019 (-) [12/2019]	336.21 (336.00) [336.21]	78.66 (0.00) [0]
835	DHANGIPIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK	3/2018	2/2020 (-) [2/2020]	217.14 (217.00) [217.14]	100.77 (0.00) [0]
836	DIGRAS DARWAH KARANJA	1/2017	6/2019 (-) [6/2020]	391.06 (391.00) [391.06]	147.00 (0.00) [12]
837	FARDAPUR TO JALGAON	2/2017	6/2019 (-) [0/0]	456.45 (-) [456.45]	71.74 (0.00) [0]
838	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS	4/2010	6/2012 (-) [0/0]	1,170.52 (-) [1,170.52]	2,051.36 (0.00) [0]
839	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4	3/2018	/ (-) [12/2020]	642.13 (-) [807.00]	395.79 (164.87) [-]
840	FOUR LANING OF AURANGABAD - YEDISHI	7/2015	1/2018 (12/2018) [3/2020]	1,871.34 (67.34) [1,871.34]	3,544.79 (0.00) [26]
841	FOUR LANNING OF TULJPUR-AUSA SECTION	2/2017	2/2020 (11/2017) [5/2020]	904.16 (911.07) [904.16]	855.25 (0.00) [3]
842	GADCHIROLI TO MUL	12/2016	6/2019 (-) [0/0]	484.15 (-) [484.15]	162.31 (0.00) [0]
843	HELWAK TO KARAD	2/2017	7/2019 (-) [0/0]	416.99 (-) [416.99]	132.40 (0.00) [0]
844	HIMAYATNAGAR TO PHULSAWANGI	3/2018	12/2019 (-) [12/2019]	294.87 (295.00) [294.87]	54.30 (0.00) [0]
845	INDAPUR TO AGARDANDA	1/2017	7/2019 (-) [12/2019]	355.17 (-) [355.17]	169.87 (0.00) [0]
846	INDAPUR TO VADPALE	1/2017	12/2019 (-) [3/2020]	1,202.52 (1,202.52) [1,202.52]	635.90 (0.00) [3]
847	JAHIRABAD TO LATUR	1/2017	11/2019 (-) [11/2019]	461.96 (461.96) [461.96]	170.43 (0.00) [0]
848	JALGAON TO BHADGAON	1/2018	11/2019 (-) [11/2019]	307.54 (308.00) [307.54]	159.59 (0.00) [0]
849	JALGAON TO NANDURA	3/2018	12/2019 (-) [12/2019]	177.84 (177.00) [177.84]	73.69 (0.00) [0]
850	JALKOT TO TOGRI	7/2018	8/2020 (-) [8/2020]	299.92 (300.00) [299.92]	19.25 (0.00) [0]
851	JINTUR TO PARBHANI	1/2017	/ (-) [0/0]	356.66 (356.66) [356.66]	49.88 (0.00) [0]
852	KAIJ TO KUSALAM	1/2017	7/2019 (-) [7/2019]	554.78 (554.78) [554.78]	184.90 (0.00) [0]
853	KALMAB TO RALEGAON	1/2017	6/2019	467.78	301.91

			(-) [0/0]	(-) [467.78]	(0.00) [0]
854	KALMATH TO ZARAP	9/2016	3/2020 (-) [3/2020]	1,338.13 (1,338.00) [1,338.13]	959.51 (0.00) [0]
855	KANTE TO WAKED	3/2016	11/2019 (-) [0/0]	1,230.02 (1,230.00) [1,230.02]	566.61 (0.00) [0]
856	KARAD PATAN CHIPLUN GUHAGAR	2/2017	6/2019 (-) [6/2020]	407.19 (407.00) [407.19]	25.00 (0.00) [12]
857	KARAD TO TAGAON	1/2017	6/2019 (-) [6/2020]	537.81 (538.00) [537.81]	98.97 (0.00) [12]
858	KARAD TO VITA	1/2018	12/2019 (-) [12/2019]	344.85 (245.00) [344.85]	98.86 (0.00) [0]
859	KARWANDI TO RAJURI	3/2018	12/2019 (-) [12/2019]	276.95 (277.00) [276.95]	107.47 (0.00) [0]
860	KATOL TO WARUD	1/2017	6/2019 (-) [8/2019]	463.62 (664.00) [463.62]	241.34 (0.00) [0]
861	KHAMGAON TO DEULGAON SAKARSHA	3/2018	12/2019 (-) [12/2019]	249.29 (-) [249.29]	116.20 (0.00) [0]
862	KHAMGAON TO SHEGAON	2/2017	5/2019 (-) [12/2019]	203.21 (203.00) [203.21]	146.79 (0.00) [0]
863	KHERDA TO NAGZARI	3/2018	12/2019 (-) [12/2019]	181.30 (-) [181.30]	111.50 (0.00) [0]
864	KOLDE TO KHETIYA	1/2017	7/2019 (-) [0/0]	509.18 (-) [509.18]	205.93 (0.00) [0]
865	KOLHA TO NASRATPUR	4/2016	4/2019 (-) [4/2020]	281.78 (282.00) [281.78]	29.73 (0.00) [12]
866	KOTHARI TO DHANORA	9/2018	8/2020 (-) [8/2020]	301.38 (301.00) [301.38]	59.42 (0.00) [0]
867	KUMBHARI PHTA TO DEULGAON RAJA	2/2017	6/2019 (-) [0/0]	406.51 (-) [406.51]	280.69 (0.00) [0]
868	KUNDRAL TO WAZAR	1/2018	12/2019 (-) [12/2019]	225.25 (225.00) [225.25]	163.75 (0.00) [0]
869	KURUDWADI TO PANDHARPUR	1/2017	7/2019 (-) [0/0]	307.63 (-) [307.63]	173.17 (0.00) [0]
870	KUSUMBA TO MALEGAON	3/2018	12/2019 (-) [12/2019]	243.45 (244.00) [243.45]	96.02 (0.00) [0]
871	LATUR TO PANGAON	3/2018	12/2019 (-) [12/2019]	336.47 (336.00) [336.47]	142.18 (0.00) [0]
872	MAHAD TO RAIGAD FORT	7/2018	5/2020 (-) [5/2020]	237.40 (-) [237.40]	8.34 (0.00) [0]
873	MAJALGAON TO KAIJ	1/2017	7/2019 (-)	413.99 (-)	299.33 (0.00)

			[7/2019]	[413.99]	[0]
874	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER	3/2018	12/2019 (-) [12/2019]	256.15 (-) [256.15]	43.50 (0.00) [0]
875	MALEGAON TO RISOD	2/2018	12/2019 (-) [12/2019]	303.24 (303.24) [303.24]	138.97 (0.00) [0]
876	MALEWADA TO CHIMUR	10/2016	6/2019 (-) [6/2020]	322.55 (-) [322.55]	184.91 (0.00) [12]
877	MANGAON TO DIGHI PORT	1/2017	7/2019 (-) [7/2020]	457.52 (457.52) [457.52]	277.98 (0.00) [12]
878	MANGRUPHIR TO MAHAN	3/2018	11/2019 (-) [11/2019]	222.13 (222.13) [222.13]	96.63 (0.00) [0]
879	MANJUSUMBA TO CHUMBALI	1/2017	8/2019 (-) [8/2019]	228.54 (228.54) [228.54]	107.30 (0.00) [0]
880	MANSAR TO SALAIKHURD	1/2018	12/2019 (-) [12/2019]	418.36 (-) [418.36]	142.13 (0.00) [0]
881	MANTHA TALUKAS BORDER TO PARTUR	1/2017	7/2019 (-) [7/2019]	486.19 (486.19) [486.19]	235.55 (0.00) [0]
882	MEHKAR TO AJISPUR	1/2017	7/2019 (-) [0/0]	232.77 (-) [232.77]	92.51 (0.00) [0]
883	MEHKAR TO CHIKALI	2/2017	5/2019 (-) [0/0]	322.48 (322.00) [322.48]	229.08 (0.00) [0]
884	MHASWAD TO TEMBHURNI	1/2017	7/2019 (-) [0/0]	488.60 (-) [488.60]	213.71 (0.00) [0]
885	MORSHI TO ACHALPUR	1/2017	6/2019 (-) [0/0]	341.16 (341.00) [341.16]	191.29 (0.00) [0]
886	MORSHI TO MAH/MP BORDER	1/2017	6/2019 (-) [0/0]	471.61 (472.00) [471.61]	288.90 (0.00) [0]
887	MUL TO CHANDRAPUR	12/2016	7/2019 (-) [7/2019]	162.34 (-) [162.34]	32.80 (0.00) [0]
888	NAGAJ TO VAJJAPUR	1/2017	6/2019 (-) [12/2019]	376.72 (377.00) [376.72]	183.81 (0.00) [0]
889	NAGBHID TO ARMORI	9/2016	7/2019 (-) [0/0]	269.05 (-) [269.05]	222.91 (0.00) [0]
890	NAGPUR RING ROAD PACKAGE-1	3/2016	7/2019 (12/2020) [12/2020]	546.00 (-) [546.00]	269.67 (0.00) [17]
891	NAGPUR RING ROAD PACKAGE-2	3/2016	7/2019 (12/2020) [12/2020]	591.66 (-) [591.66]	310.56 (0.00) [17]
892	NAIGAONBANDI TO MANGRULPIR	12/2017	3/2019 (-) [12/2019]	244.04 (244.00) [244.04]	44.94 (0.00) [0]
893	NALDURG TO AKKALKOT	2/2018	12/2019 (-) [12/2019]	274.50 (275.00) [274.50]	66.39 (0.00) [0]

894	NANDED TO JALKOT	12/2017	9/2019 (-) [9/2019]	456.93 (457.00) [456.93]	87.95 (0.00) [0]
895	NANDGAON TO MORSHI	1/2017	6/2019 (-) [12/2019]	385.87 (386.00) [385.87]	232.75 (0.00) [0]
896	NASHIK TO PETH	12/2015	11/2018 (-) [11/2019]	289.60 (-) [289.60]	129.81 (0.00) [0]
897	NASRATPUR TO BARASGAON	7/2016	9/2019 (-) [9/2019]	406.54 (406.54) [406.54]	147.00 (0.00) [0]
898	NILAJPHATA TO BHANDARA	1/2018	5/2020 (-) [5/2020]	420.63 (421.00) [420.63]	50.60 (0.00) [0]
899	OMREGA TO AUSA	3/2018	12/2019 (-) [12/2019]	272.04 (272.00) [272.04]	164.24 (0.00) [0]
900	OSMANNAGAR TO KUNDRAL	9/2017	8/2020 (-) [8/2020]	344.25 (344.00) [344.25]	71.18 (0.00) [0]
901	PAHUR TO BODHWAD	1/2017	5/2020 (-) [5/2020]	244.93 (-) [244.93]	75.23 (0.00) [0]
902	PAITHAN TO SHIRUR	3/2017	6/2019 (-) [0/0]	341.80 (-) [341.80]	107.89 (0.00) [0]
903	PALPHATA TO PHULAMBAR	3/2018	12/2019 (-) [12/2019]	227.19 (227.00) [227.19]	80.23 (0.00) [0]
904	PANCHARAL TO MANDANGHAR	7/2018	5/2020 (-) [5/2020]	381.08 (302.00) [381.08]	13.03 (0.00) [0]
905	PANDHARPUR TO SANGOLA	7/2017	7/2019 (-) [0/0]	218.38 (-) [218.38]	168.75 (0.00) [0]
906	PARBHANI TO GANGKHED	3/2018	12/2019 (-) [12/2019]	238.19 (238.00) [238.19]	56.85 (0.00) [0]
907	PARLI PIMPLA DAHIGUDA	2/2017	6/2019 (-) [6/2020]	205.72 (205.72) [205.72]	30.42 (0.00) [12]
908	PARSHURAM GHAT TO ARAWALI	4/2016	12/2019 (-) [0/0]	983.14 (983.00) [983.14]	655.15 (0.00) [0]
909	PARTUR TO MAJALGAON	1/2017	7/2019 (-) [7/2019]	420.57 (420.57) [420.57]	186.39 (0.00) [0]
910	PATGAON KHOPOLI SECTION I	1/2018	12/2019 (-) [12/2019]	170.00 (-) [170.00]	56.57 (0.00) [0]
911	PEN TO KHOPOLI	3/2018	3/2018 (-) [12/2019]	301.39 (302.00) [301.39]	17.09 (0.00) [0]
912	PIMPLA TO MANJARSUMBHA	1/2017	8/2019 (-) [8/2019]	595.77 (595.77) [595.77]	171.44 (0.00) [0]
913	PUNE RAIGARH DISTRICT BORDER TO MANGAON	3/2018	12/2019 (-) [12/2019]	223.46 (-) [223.46]	21.42 (0.00) [0]
914	PUNE TO MALE VILLAGE	3/2018	12/2019	228.31	19.50

			(-) [12/2019]	(-) [228.31]	(0.00) [0]
915	PUNE-SATARA(NH-4)	10/2010	3/2013 (-) [3/2020]	1,724.55 (-) [1,724.55]	2,442.58 (0.00) [84]
916	RALEGAON TO RAMTIRTH	1/2017	7/2019 (-) [0/0]	210.81 (-) [210.81]	120.69 (0.00) [0]
917	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00	1/2014	/ (-) [0/0]	446.77 (-) [446.77]	278.50 (0.00) [0]
918	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM	1/2015	/ (-) [0/0]	225.81 (-) [225.81]	85.11 (0.00) [0]
919	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA	3/2016	12/2019 (-) [12/2019]	536.65 (356.00) [536.65]	472.99 (0.00) [0]
920	RISOD TO HINGOLI	2/2018	12/2019 (-) [12/2019]	355.99 (355.99) [355.99]	175.97 (0.00) [0]
921	SAKOLI TO BHANDARA	1/2017	6/2019 (-) [11/2019]	362.96 (362.96) [362.96]	37.83 (0.00) [0]
922	SALAIKHURD TO TIRORA	1/2018	12/2019 (-) [12/2019]	415.25 (415.25) [415.25]	111.22 (0.00) [0]
923	SANGOLA TO JATH	1/2018	12/2019 (-) [12/2019]	257.38 (257.00) [257.38]	94.15 (0.00) [0]
924	SARAD VANI PIMPALGAON	1/2017	7/2019 (-) [0/0]	250.46 (-) [250.46]	107.63 (0.00) [0]
925	SARSAM TO KOTHARI	2/2016	7/2019 (-) [0/0]	545.64 (-) [545.64]	113.53 (0.00) [0]
926	SATARA MURVAD PILLOV PANDHARPUR	1/2017	/ (-) [0/0]	388.44 (-) [388.44]	191.77 (0.00) [0]
927	SATARA TO MHASWAD	1/2017	7/2019 (-) [0/0]	653.46 (-) [653.46]	240.42 (0.00) [0]
928	SELDOH TO PANVAR	7/2018	5/2020 (-) [5/2020]	404.33 (404.00) [404.33]	44.19 (0.00) [0]
929	SHAHPUR PATGAON SECTION I	1/2018	12/2019 (-) [12/2019]	150.79 (150.79) [150.79]	21.42 (0.00) [0]
930	SHEGAON TO DEORI PHATA	2/2017	5/2019 (-) [12/2019]	373.10 (373.00) [373.10]	163.43 (0.00) [0]
931	SHIROD SHAHPURER TO NANDED	1/2017	7/2019 (-) [7/2019]	211.34 (211.34) [211.34]	104.83 (0.00) [0]
932	SHIRUR TO KHARDA	2/2017	6/2019 (-) [0/0]	381.77 (-) [381.77]	157.79 (0.00) [0]
933	SHIVUR TO YEOLA	3/2018	12/2019 (-) [12/2019]	181.08 (-) [181.08]	7.50 (0.00) [0]
934	SILLOD TO FARDAPUR	2/2017	6/2019 (-)	337.46 (-)	52.22 (0.00)

			[0/0]	[337.46]	[0]
935	SIX LANE OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH	12/2017	/ (-) [10/2020]	404.94 (448.18) [448.18]	193.77 (43.24) [-]
936	SIX LANE FROM EXISTING KM 494.410(DSIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DSIGN CHAINAGE	11/2016	/ (3/2020) [3/2020]	290.73 (315.00) [315.00]	246.70 (24.27) [-]
937	TAKARKHED TO JALNA	9/2017	6/2019 (-) [12/2019]	417.90 (418.00) [417.90]	138.26 (0.00) [0]
938	TALEGAON TO GONAPUR	1/2018	3/2019 (-) [12/2019]	264.41 (264.00) [264.41]	53.71 (0.00) [0]
939	TALGAON TO KALMATH	10/2016	3/2020 (-) [3/2020]	904.70 (905.00) [904.70]	604.05 (0.00) [0]
940	TASGAON TO SHIRDHON	1/2017	11/2019 (-) [11/2019]	195.64 (196.00) [195.64]	169.73 (0.00) [0]
941	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI	2/2017	7/2019 (-) [0/0]	422.02 (422.00) [422.02]	247.01 (0.00) [0]
942	VADPALE TO BHOGAN KHURD	1/2017	11/2019 (-) [3/2020]	1,598.47 (1,560.00) [1,598.47]	768.91 (0.00) [4]
943	VITA TO NAGAJ	3/2018	12/2019 (-) [12/2019]	304.58 (305.00) [304.58]	24.82 (0.00) [0]
944	WADI TO ASOLA	1/2017	9/2019 (-) [9/2020]	363.82 (363.82) [363.82]	92.10 (0.00) [12]
945	WADIGODRI TO DHANGRIPIMPRI	3/2018	2/2020 (-) [2/2020]	194.23 (194.00) [194.23]	88.23 (0.00) [0]
946	WAKAN PALI KHOPOLI	1/2017	5/2019 (-) [5/2020]	376.19 (376.19) [376.19]	37.03 (0.00) [12]
947	WAKED TO TALEGAON	2/2016	2/2019 (-) [0/0]	1,244.75 (1,245.00) [1,244.75]	357.60 (0.00) [0]
948	WARDHA TO ARVI	2/2018	4/2020 (-) [4/2020]	313.58 (313.58) [313.58]	32.96 (0.00) [0]
949	WARDHA TO HINGAGHAT	1/2018	12/2019 (-) [12/2019]	216.90 (216.90) [216.90]	82.54 (0.00) [0]
950	WASHIM TO DASTAPUR	3/2018	12/2019 (-) [12/2019]	165.51 (-) [165.51]	83.45 (0.00) [0]
951	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16	10/2015	/ (-) [0/0]	289.60 (-) [289.60]	90.65 (0.00) [0]
952	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	5/2013	2/2014 (-) [0/0]	1,348.20 (-) [1,348.20]	1,792.90 (0.00) [0]
	Telecommunications				
953	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	1/2018	10/2018 (2/2020) [2/2020]	231.80 (240.10) [240.10]	119.92 (8.30) [16]
	Urban Development				
954	CONSTRUCTION OF IITB RESEARCH PARK AT IIT	1/2018	7/2020	223.37	48.89

	BOMBAY, POWAI, MUMBAI		(12/2020) [12/2020]	(-) [223.37]	(0.00) [5]
955	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	7/2013	1/2015 (-) [5/2020]	23,136.00 (-) [23,136.00]	0.00 (0.00) [64]
956	NAGPUR METRO RAIL	8/2014	3/2018 (-) [12/2019]	8,680.00 (-) [8,680.00]	6,639.30 (0.00) [0]
957	PUNE METRO RAIL PROJECT (PHASE 1)	12/2016	11/2021 (3/2022) [3/2022]	11,420.00 (11,420.00) [11,420.00]	3,614.06 (0.00) [4]
958	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA	6/2010	3/2012 (-) [12/2019]	205.00 (-) [205.00]	166.12 (0.00) [0]
	<u>Water Resources</u>				
959	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA	3/2017	12/2019 (-) [0/0]	233.57 (-) [233.57]	32.20 (0.00) [0]
	<u>MANIPUR</u>				
	<u>Power</u>				
960	LOKTAK D/S HEP(NHPC)	12/1999	6/2006 (-) [0/0]	578.62 (-) [578.62]	0.00 (0.00) [0]
	<u>Railways</u>				
961	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (-) [3/2022]	4,454.17 (13,809.00) [12,524.00]	9,599.02 (8,069.83) [132]
	<u>Road Transport And Highways</u>				
962	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260.	10/2016	11/2020 (-) [11/2020]	235.31 (-) [235.31]	97.25 (0.00) [0]
963	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	8/2017	10/2018 (-) [10/2021]	517.57 (-) [457.77]	137.04 (-59.80) [36]
	<u>Urban Development</u>				
964	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	2/2014	3/2015 (-) [10/2020]	216.69 (-) [216.69]	52.00 (0.00) [67]
	<u>MEGHALAYA</u>				
	<u>Health And Family Welfare</u>				
965	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (-) [7/2020]	363.99 (-) [363.99]	219.50 (0.00) [26]
	<u>Human Resource Development</u>				
966	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	9/2013	9/2014 (-) [12/2020]	484.32 (-) [626.26]	0.00 (141.94) [75]
	<u>Railways</u>				
967	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [3/2021]	906.46 (-) [6,000.60]	263.12 (5,094.14) [0]
	<u>Road Transport And Highways</u>				
968	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	3/2019	5/2019 (-) [0/0]	306.28 (-) [306.28]	53.09 (0.00) [0]
969	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	12/2015	5/2018 (3/2018) [10/2019]	479.20 (-) [479.20]	712.89 (0.00) [0]
970	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	/ (-) [9/2021]	553.51 (-) [553.51]	44.39 (0.00) [-]

	<u>Urban Development</u>				
971	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR	4/2014	9/2017 (-) [0/0]	151.33 (-) [151.33]	7.15 (0.00) [0]
	<u>MIZORAM</u>				
	<u>Railways</u>				
972	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (3/2022) [3/2022]	2,393.47 (4,968.00) [5,021.45]	3,183.01 (2,627.98) [96]
	<u>Road Transport And Highways</u>				
973	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (12/2020) [6/2020]	195.04 (-) [377.99]	312.41 (182.95) [116]
974	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	9/2014 (6/2020) [6/2020]	186.96 (-) [305.61]	279.13 (118.65) [69]
975	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (6/2021) [6/2021]	193.69 (-) [327.92]	258.71 (134.23) [128]
976	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	519.09 (-) [519.09]	22.52 (0.00) [0]
977	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	428.11 (-) [428.11]	0.00 (0.00) [0]
978	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	537.82 (-) [537.82]	0.00 (0.00) [0]
979	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	640.07 (-) [640.07]	0.00 (0.00) [0]
980	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	473.18 (-) [473.18]	0.00 (0.00) [0]
981	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	518.53 (-) [518.53]	0.00 (0.00) [0]
982	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	642.96 (-) [642.96]	0.00 (0.00) [0]
983	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	404.29 (-) [404.29]	0.00 (0.00) [0]
984	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (12/2020) [12/2020]	624.41 (-) [992.67]	886.01 (368.26) [117]
	<u>MULTI STATE</u>				
	<u>Coal</u>				
985	DHANKASA UG (1.00 MTY)	9/2016	3/2022 (-) [3/2022]	458.07 (-) [458.07]	22.46 (0.00) [0]
986	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY)	2/2017	3/2021 (-) [3/2021]	328.00 (-) [328.00]	186.61 (0.00) [0]
987	NILJAI EXPANSION (DEEP) OC (3.5 MTY)	8/2016	3/2022 (-) [3/2022]	319.76 (-) [319.76]	190.69 (0.00) [0]
	<u>Commerce And Industry</u>				
988	DELHI MUMBAI INDUSTRIAL CORRIDOR	9/2011	9/2019 (-) [9/2020]	12,579.09 (-) [12,579.09]	778.93 (0.00) [12]

	Human Resource Development				
989	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION	8/2018	3/2019 (-) [0/0]	418.00 (-) [418.00]	110.00 (0.00) [0]
990	STUDY IN INDIA	3/2018	4/2018 (-) [0/0]	150.00 (-) [150.00]	0.00 (0.00) [0]
	Petroleum				
991	50MW WIND ENERGY POWER PROJECT	11/2015	6/2017 (-) [0/0]	500.00 (-) [500.00]	0.00 (0.00) [0]
992	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	1/2015	12/2020 (-) [12/2020]	1,823.00 (3,027.90) [3,027.90]	1,030.43 (1,204.90) [0]
993	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II	9/2016	12/2019 (6/2020) [6/2020]	571.66 (-) [571.66]	372.70 (0.00) [6]
994	BARAUNI-GUWAHATI PIPELINE	6/2018	12/2021 (-) [12/2021]	3,308.00 (-) [3,308.00]	1,433.56 (0.00) [0]
995	BOKARO-ANGUL PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	3,437.00 (-) [3,437.00]	1,326.48 (0.00) [0]
996	DOBHI-DURGAPUR PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	2,433.00 (-) [2,433.00]	1,566.59 (0.00) [0]
997	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	9/2017	3/2021 (-) [3/2021]	2,677.00 (-) [2,677.00]	1,106.90 (0.00) [0]
998	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	6/2009	12/2012 (2/2022) [2/2022]	2,915.00 (4,915.00) [4,915.00]	2,784.58 (2,000.00) [110]
999	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT	7/2015	12/2020 (-) [12/2020]	2,881.40 (-) [2,000.00]	1,326.88 (-881.40) [0]
1000	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION	9/2016	6/2020 (-) [6/2020]	1,879.00 (-) [1,879.00]	1,590.22 (0.00) [0]
1001	PARADIP HYDERABAD PIPELINE	1/2015	12/2020 (-) [8/2020]	2,321.00 (3,338.00) [3,338.00]	2,123.21 (1,017.00) [-4]
1002	PARADIP LPG IMPORT FACILITY	1/2015	7/2018 (-) [10/2020]	690.00 (-) [690.00]	351.04 (0.00) [27]
1003	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I)	5/2016	10/2020 (-) [10/2020]	406.00 (-) [406.00]	106.50 (0.00) [0]
1004	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	7/2011	3/2017 (6/2020) [6/2020]	352.56 (-) [438.84]	268.45 (86.28) [39]
	Power				
1005	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION)	9/2017	9/2019 (2/2020) [2/2020]	198.49 (-) [198.49]	126.26 (0.00) [5]
1006	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	12/2018 (-) [12/2020]	4,754.42 (-) [9,072.36]	1,402.48 (4,317.94) [24]
1007	EASTERN REGION STRENGTHENING SCHEME XX	11/2017	5/2020 (-) [5/2020]	358.83 (-) [358.83]	177.36 (0.00) [0]
1008	EASTERN REGION STRENGTHENING SCHEME-V	10/2013	4/2016	1,364.52	1,283.60

			(8/2019) [2/2020]	(1,891.41) [1,891.41]	(526.89) [46]
1009	EASTERN REGION STRENGTHENING SCHEME-XII	5/2014	11/2016 (6/2020) [3/2020]	522.29 (546.36) [546.36]	470.71 (24.07) [40]
1010	EASTERN REGION STRENGTHENING SCHEME-XVIII	3/2017	7/2020 (-) [7/2020]	3,500.00 (3,500.00) [3,500.00]	2,039.35 (0.00) [0]
1011	EASTERN REGION STRENGTHENING SCHEME XVII(PART B)	2/2017	6/2019 (-) [3/2020]	235.53 (-) [235.53]	138.98 (0.00) [9]
1012	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/	2/2017	2/2019 (4/2020) [3/2020]	322.30 (-) [322.30]	166.84 (0.00) [13]
1013	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	3/2015	3/2018 (-) [3/2020]	197.40 (197.40) [197.40]	85.34 (0.00) [24]
1014	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D	5/2016	5/2019 (-) [2/2020]	3,519.59 (-) [3,519.59]	2,562.41 (0.00) [9]
1015	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR	2/2017	4/2020 (-) [4/2020]	5,070.13 (-) [5,070.13]	3,270.48 (0.00) [0]
1016	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALAR-NORTH TRICHUR-SCHEME-I: RAIGARH-P	5/2016	11/2019 (-) [3/2020]	14,733.37 (-) [14,733.37]	9,883.31 (0.00) [4]
1017	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALAR EN	8/2017	2/2020 (-) [6/2020]	1,931.39 (-) [1,931.39]	1,164.36 (0.00) [4]
1018	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	12/2014	12/2018 (-) [12/2020]	5,111.33 (-) [6,880.36]	1,886.30 (1,769.03) [24]
1019	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	2/2009	8/2013 (3/2022) [3/2022]	11,130.19 (14,719.10) [14,719.10]	12,824.45 (3,588.91) [103]
1020	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO	3/2017	11/2019 (-) [11/2019]	283.72 (-) [283.72]	196.10 (0.00) [0]
1021	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	12/2015	4/2019 (-) [1/2020]	3,654.00 (-) [3,654.00]	3,508.04 (0.00) [9]
1022	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	10/2016	4/2019 (-) [1/2020]	608.24 (-) [608.24]	425.04 (0.00) [9]
1023	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII	1/2015	7/2017 (6/2019) [1/2020]	203.28 (260.03) [260.03]	200.16 (56.75) [30]
1024	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII	3/2017	12/2019 (-) [3/2020]	379.95 (-) [379.95]	113.54 (0.00) [3]
1025	SYSTEM STRENGTHENING XIII OF SR GRID	10/2011	6/2014 (9/2019) [2/2020]	487.49 (639.46) [639.46]	590.30 (151.97) [68]
1026	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	10/2008	10/2012 (12/2019) [3/2020]	4,824.12 (5,071.94) [5,071.94]	4,595.36 (247.82) [89]
1027	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP)	1/2015	10/2017 (9/2019) [3/2020]	871.62 (-) [871.62]	606.81 (0.00) [29]
1028	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II	10/2016	1/2019 (9/2019)	408.46 (-)	322.79 (0.00)

	(PART II)		[3/2020]	[408.46]	[14]
1029	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH	6/2014	3/2018 (12/2019) [3/2020]	5,151.37 (5,151.37) [5,151.37]	3,269.93 (0.00) [24]
1030	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	3/2016	1/2018 (3/2020) [3/2020]	808.63 (-) [808.63]	547.80 (0.00) [26]
1031	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	1/2014	4/2016 (12/2017) [3/2020]	374.63 (374.63) [374.63]	224.83 (0.00) [47]
	<u>Railways</u>				
1032	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT	12/2015	12/2023 (12/2023) [12/2023]	1,08,000.00 (-) [1,08,000.00]	6,708.69 (0.00) [0]
1033	BANDEL-BOINCHI 3RD LINE	4/2011	/ (-) [3/2020]	288.35 (-) [402.48]	402.48 (114.13) [-]
1034	BARIARPUR-MANANPUR VIA KHARAGPUR, LACHIMPUR-BARAHAT	4/2007	/ (-) [3/2025]	450.55 (-) [250.55]	20.12 (-200.00) [-]
1035	BHADRACHALAM ROAD-SATTUPALLI	4/2010	3/2020 (3/2020) [3/2020]	704.31 (927.94) [927.94]	303.24 (223.63) [0]
1036	BHADRACHALAM-KOVVUR	4/2012	/ (-) [0/0]	923.23 (2,184.83) [2,184.83]	2.46 (1,261.60) [0]
1037	BOINCHI-SHAKTIGARH 3RD LINE	4/2011	/ (-) [3/2021]	175.80 (-) [260.83]	260.83 (85.03) [-]
1038	CHANDIGARH-BADDI	4/2007	3/2023 (-) [3/2023]	328.14 (-) [1,540.00]	234.79 (1,211.86) [0]
1039	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA	4/2003	/ (-) [3/2025]	337.96 (-) [336.96]	70.20 (-1.00) [-]
1040	CHENNAI-CUDDALORE VIA MAMALLAPURAM	4/2008	/ (-) [0/0]	523.52 (-) [2,300.00]	2.28 (1,776.48) [0]
1041	CHHAPRA-BALLIA UP	3/2013	1/2019 (-) [1/2020]	295.00 (-) [477.31]	370.93 (182.31) [12]
1042	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP	3/2007	12/2021 (-) [12/2021]	243.78 (-) [895.00]	106.55 (651.22) [0]
1043	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	4/2005	3/2017 (-) [3/2025]	595.51 (-) [769.40]	103.08 (173.89) [96]
1044	CHOTTAUDEPUR-DHAR(NL)	4/2007	3/2022 (3/2022) [3/2022]	1,347.26 (1,347.26) [1,347.26]	756.98 (0.00) [0]
1045	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	4/2007	3/2022 (3/2023) [3/2023]	1,640.04 (1,640.04) [1,640.04]	756.11 (0.00) [12]
1046	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL	4/2010	3/2017 (-) [3/2025]	365.17 (-) [296.43]	275.76 (-68.74) [96]
1047	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL	4/2007	/ (-) [3/2022]	336.91 (-) [791.39]	517.05 (454.48) [-]
1048	DEOGHAR - SULTANGANJ (INL), ER	4/2000	2/2013 (-)	607.09 (-)	637.56 (818.35)

			[3/2024]	[1,425.44]	[133]
1049	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	4/2010	/ (-) [0/0]	2,030.50 (-) [2,030.50]	19.07 (0.00) [0]
1050	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	4/2010	3/2015 (3/2025) [3/2025]	651.00 (-) [1,009.00]	7.96 (358.00) [120]
1051	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	/ (-) [0/0]	11,589.00 (30,357.00) [28,181.00]	0.00 (16,592.00) [0]
1052	GAYA-CHATRA (NL)	4/2008	/ (-) [0/0]	415.67 (-) [549.75]	15.55 (134.08) [0]
1053	GONDIA-JABALPUR(GC),(SECR)	2/1997	4/2020 (1/2021) [1/2021]	511.86 (1,756.00) [1,756.00]	1,679.29 (1,244.14) [9]
1054	GOOTY-DHARMAVARAM-BANGLORE	4/2015	/ (-) [0/0]	636.38 (-) [636.38]	0.00 (0.00) [0]
1055	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	4/2011	3/2022 (-) [12/2024]	2,912.96 (-) [3,845.60]	148.26 (932.64) [33]
1056	HAJIPUR - BACHAWARA	5/2015	3/2019 (-) [2/2021]	678.54 (678.54) [678.54]	556.86 (0.00) [23]
1057	HANSDIHA-GODDA NL	4/2011	3/2020 (-) [3/2021]	542.18 (-) [693.80]	474.79 (151.62) [12]
1058	HANSNABAD-HINGALGANJ NEW BG LINE	4/2010	/ (-) [3/2025]	172.03 (-) [260.10]	10.73 (88.07) [-]
1059	HATHUA-BHATNI (N L) (NER)	4/2005	12/2022 (-) [12/2022]	230.03 (-) [230.03]	277.14 (0.00) [0]
1060	HOTGI-KUDGI-GADAG	3/2015	3/2019 (-) [3/2021]	1,614.59 (1,870.41) [1,870.41]	1,056.97 (255.82) [24]
1061	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS)	4/2010	11/2018 (-) [3/2021]	157.94 (-) [157.94]	51.75 (0.00) [28]
1062	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGREGATION OF ARRIVAL/DEPARTURE AND OTHER AMENITIES	4/2011	/ (-) [3/2025]	166.89 (-) [166.89]	0.02 (0.00) [-]
1063	JALANDHAR-PATHANKOT-JAMMU TAWI	3/2002	3/2016 (-) [3/2021]	625.00 (-) [859.00]	835.35 (234.00) [60]
1064	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	4/2008	3/2014 (-) [3/2024]	2,132.77 (2,132.77) [2,132.77]	350.17 (0.00) [120]
1065	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONG WITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3	4/2001	3/2016 (-) [3/2025]	923.52 (-) [995.10]	507.56 (71.58) [108]
1066	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE	4/2010	/ (-) [3/2025]	174.56 (-) [174.56]	71.42 (0.00) [-]
1067	KAZIPET-BALHRSHA	4/2015	3/2021 (-) [3/2023]	2,063.03 (2,063.03) [2,063.03]	880.17 (0.00) [24]
1068	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	4/2012	3/2023 (-) [3/2024]	1,856.95 (1,952.68) [1,952.68]	329.00 (95.73) [12]

1069	KURUPPANTHARA-CHINGAVANAM	4/2007	/ (-) [0/0]	270.14 (-) [457.08]	373.51 (186.94) [0]
1070	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	4/1987	3/2006 (-) [3/2025]	406.99 (-) [545.70]	148.49 (138.71) [228]
1071	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	9/1998	5/2008 (-) [3/2023]	247.66 (-) [8,248.50]	1,986.78 (8,000.84) [178]
1072	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL	4/2009	3/2014 (-) [3/2025]	257.42 (-) [257.42]	108.11 (0.00) [132]
1073	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	4/2011	3/2019 (-) [12/2019]	120.70 (-) [1,800.00]	187.92 (1,679.30) [0]
1074	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	4/2009	2/2012 (-) [3/2025]	499.96 (-) [680.68]	159.70 (180.72) [157]
1075	MONIGRAM- NIMITTA	4/2012	/ (-) [3/2024]	250.93 (-) [310.70]	287.10 (59.77) [-]
1076	MUNEERABAD-MAHABOBNAGAR(NL),SCR	4/1997	3/2000 (-) [3/2021]	1,723.00 (1,780.29) [3,472.59]	970.69 (1,749.59) [252]
1077	MURKONGSELEK-PASIGHAT NL	4/2011	3/2020 (-) [3/2020]	414.84 (-) [661.00]	123.00 (246.16) [0]
1078	NANGALDAM-TALWARA(NL),NR	3/1981	7/2012 (-) [3/2024]	450.00 (2,010.00) [2,200.00]	668.77 (1,750.00) [140]
1079	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL	4/2010	3/2005 (-) [3/2025]	494.54 (-) [494.59]	32.00 (0.05) [240]
1080	NEW BG LINE FROM BALURGHAT TO HILLY NFR	4/2010	3/2020 (-) [3/2020]	242.22 (-) [471.00]	69.09 (228.78) [0]
1081	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	4/2010	/ (-) [6/2021]	241.52 (-) [373.87]	273.20 (132.35) [-]
1082	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	4/2013	3/2019 (-) [0/0]	1,798.00 (-) [2,496.67]	0.04 (698.67) [0]
1083	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	4/1999	/ (-) [0/0]	819.23 (-) [1,871.00]	1,082.01 (1,051.77) [0]
1084	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	4/2000	12/2008 (-) [3/2021]	1,180.19 (3,300.00) [4,541.00]	3,346.08 (3,360.81) [147]
1085	PHULERA - DIGANA DOUBLING	5/2015	3/2020 (-) [4/2022]	600.00 (-) [685.99]	99.38 (85.99) [25]
1086	PIRPAINTI-BHAGALPUR	4/2011	/ (-) [5/2019]	261.38 (-) [492.84]	492.84 (231.46) [0]
1087	PIRPAINTI-JASIDIH	4/2013	3/2022 (-) [3/2025]	915.98 (-) [2,137.81]	300.18 (1,221.83) [36]
1088	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY	4/2011	3/2017 (-) [3/2026]	299.60 (-) [335.62]	1.12 (36.02) [108]
1089	RATLAM-DUNGARPUR VIA BANSWARA (NL)	4/2011	/	2,082.75	185.90

			(-) [0/0]	(-) [4,262.36]	(2,179.61) [0]
1090	RAYADURGA-TUMKUR NL	4/2007	/	2,062.30	932.12
			(-) [3/2025]	(2,062.30) [2,062.30]	(0.00) [-]
1091	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL	4/2000	/	297.47	52.09
			(-) [3/2025]	(-) [298.22]	(0.75) [-]
1092	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	4/2010	3/2016	277.28	169.37
			(-) [3/2025]	(-) [266.32]	(-10.96) [108]
1093	SRINIVASA-PURA-MADANAPALLI NL	4/2013	/	296.00	0.00
			(-) [12/2023]	(466.65) [466.65]	(170.65) [-]
1094	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR	4/2007	/	450.00	0.00
			(-) [3/2025]	(-) [1,261.34]	(811.34) [-]
1095	TARAKESHWAR-MAGRA NEW BG LINE	4/2010	/	365.17	1.76
			(-) [3/2025]	(-) [527.54]	(162.37) [-]
1096	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	3/2020	16,592.00	22,485.00
			(-) [3/2020]	(51,101.00) [51,101.00]	(34,509.00) [0]
1097	YELAHANKA-PENUKONDA	5/2015	3/2020	860.43	781.04
			(-) [3/2020]	(-) [958.00]	(97.57) [0]
	<u>Road Transport And Highways</u>				
1098	4 LANING OF NAGPUR-BETUL	2/2011	8/2014	2,498.76	2,531.46
			(-) [0/0]	(-) [2,498.76]	(0.00) [0]
1099	DELHI AGRA APPROVED LENGTH 180.0 KM	10/2012	4/2015	1,928.22	2,467.00
			(1/2017) [6/2020]	(-) [2,945.00]	(1,016.78) [62]
1100	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67.	3/2018	/	1,294.47	0.00
			(-) [0/0]	(-) [1,296.00]	(1.53) [0]
1101	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE	3/2018	/	998.70	0.00
			(-) [0/0]	(-) [962.00]	(-36.70) [0]
1102	GWALIOR-JHANSI, NH-75	12/2003	12/2009	604.00	237.64
			(8/2020) [3/2020]	(364.59) [364.59]	(-239.41) [123]
1103	MUZAFFARNAGAR-HARIDWAR	9/2011	3/2013	754.00	1,364.18
			(11/2019) [11/2020]	(-) [754.00]	(0.00) [92]
1104	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP	9/2016	/	1,244.10	1,445.00
			(-) [2/2020]	(-) [1,244.10]	(0.00) [-]
1105	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	2/2009	8/2011	1,693.75	2,848.49
			(-) [0/0]	(2,848.49) [1,693.75]	(0.00) [0]
1106	VARANASI-AURANGABAD KM.786 TO KM.978.40	9/2011	3/2014	2,848.00	1,159.10
			(4/2017) [6/2020]	(-) [2,848.00]	(0.00) [75]
	<u>Shipping And Ports</u>				
1107	JAL MARG VIKAS PROJECT	1/2018	3/2023	4,200.00	1,540.69
			(3/2023) [3/2023]	(5,369.18) [5,369.18]	(1,169.18) [0]
	<u>Telecommunications</u>				
1108	NETWORK FOR SPECTRUM	3/2012	7/2015	13,334.00	12,146.00
			(-)	(-)	(11,330.00)

			[5/2020]	[24,664.00]	[58]
1109	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY	9/2014	9/2014 (-) [0/0]	2,111.17 (-) [2,011.17]	253.90 (-100.00) [0]
	<u>Urban Development</u>				
1110	DELHI GHAZIABAD MEERUT RRTS CORRIDOR	3/2019	6/2025 (-) [6/2025]	30,274.00 (-) [30,274.00]	690.64 (0.00) [0]
	<u>NAGALAND</u>				
	<u>Railways</u>				
1111	DIMAPUR-TIZIT NL	4/2013	3/2020 (-) [3/2020]	4,274.00 (-) [4,274.00]	0.00 (0.00) [0]
1112	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015 (-) [10/2021]	2,326.52 (-) [5,806.81]	876.09 (3,480.29) [79]
	<u>Road Transport And Highways</u>				
1113	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018 (5/2019) [0/0]	239.30 (174.70) [174.70]	9.17 (-64.60) [0]
1114	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	3/2018	9/2018 (-) [0/0]	285.68 (-) [285.68]	9.58 (0.00) [0]
1115	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	3/2018	9/2018 (11/2018) [0/0]	282.98 (192.60) [192.60]	24.57 (-90.38) [0]
1116	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018 (-) [8/2020]	387.00 (-) [387.00]	145.18 (0.00) [23]
1117	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	9/2018 (-) [0/0]	500.09 (336.49) [336.49]	0.00 (-163.60) [0]
1118	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN	3/2017	11/2020 (-) [11/2020]	217.35 (-) [217.35]	35.10 (0.00) [0]
1119	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683	2/2017	4/2017 (-) [0/0]	507.68 (-) [507.68]	129.13 (0.00) [0]
1120	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (7/2019) [0/0]	339.57 (233.35) [233.35]	10.15 (-106.22) [0]
1121	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	3/2018	9/2018 (-) [0/0]	315.03 (-) [315.03]	18.60 (0.00) [0]
1122	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	9/2018 (-) [0/0]	240.64 (-) [240.64]	25.98 (0.00) [0]
1123	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [0/0]	215.12 (-) [215.12]	29.88 (0.00) [0]
1124	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	9/2018 (-) [0/0]	215.79 (-) [215.79]	16.54 (0.00) [0]
1125	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [0/0]	272.89 (-) [272.89]	0.00 (0.00) [0]
1126	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	3/2018	9/2018 (-) [0/0]	323.98 (-) [323.98]	0.00 (0.00) [0]
1127	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900	3/2018	9/2018 (11/2018)	251.97 (160.10)	18.67 (0.00)

	TO KM40.0		[0/0]	[251.97]	[0]
1128	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (11/2018) [0/0]	237.72 (136.73) [237.72]	45.85 (0.00) [0]
1129	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	8/2016 (-) [3/2020]	373.07 (387.00) [387.00]	216.07 (13.93) [43]
1130	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2016 (-) [6/2020]	396.52 (339.55) [339.55]	237.99 (-56.97) [46]
1131	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	3/2016	8/2016 (-) [3/2020]	429.52 (340.00) [340.00]	189.88 (-89.52) [43]
1132	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M	11/2016	9/2019 (-) [0/0]	336.25 (-) [336.25]	62.64 (0.00) [0]
1133	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (-) [12/2020]	172.63 (-) [172.63]	77.30 (0.00) [0]
1134	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (-) [12/2020]	167.62 (-) [167.62]	61.37 (0.00) [0]
1135	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA	12/2010	2/2011 (-) [0/0]	1,296.00 (-) [1,296.00]	0.00 (0.00) [0]
1136	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH-	3/2019	12/2022 (-) [12/2022]	237.51 (-) [237.51]	0.00 (0.00) [0]
	<u>ODISHA</u>				
	<u>Coal</u>				
1137	ANANTA OC EXPANSION PH-III (15.0 MTY)	8/2008	3/2012 (-) [3/2021]	207.28 (-) [207.28]	306.94 (0.00) [108]
1138	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	3/2010 (-) [3/2022]	172.08 (-) [172.08]	377.07 (0.00) [144]
1139	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	5/2014	3/2019 (-) [3/2024]	479.15 (-) [479.15]	214.07 (0.00) [60]
1140	BHUBANESWARI OCP, MCL (20.0 MTY)	12/2007	3/2017 (-) [3/2021]	490.10 (-) [490.10]	524.33 (0.00) [48]
1141	GARJANBAHAL OCP	11/2014	3/2021 (-) [3/2021]	1,375.38 (-) [1,375.38]	445.23 (0.00) [0]
1142	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	3/2013 (-) [3/2022]	479.53 (-) [479.53]	445.05 (0.00) [108]
1143	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP	5/2018	3/2027 (-) [3/2027]	2,434.75 (-) [2,434.75]	140.36 (0.00) [0]
1144	JAGANNATH RE-ORGANISATION OC.(6.00 MTY)	5/2014	3/2019 (-) [3/2021]	337.66 (-) [337.66]	215.55 (0.00) [24]
1145	KANIHA OCP, MCL, (10.0 MTY)	12/2007	3/2013 (-) [3/2022]	457.77 (-) [457.77]	568.14 (0.00) [108]
1146	KULDA EXPN OC. (5.00 MTY)	6/2014	3/2018 (-) [3/2021]	289.03 (-) [289.03]	0.00 (0.00) [36]
1147	KULDA OCP (MAHANADI COALFIELDS LTD)	1/2005	3/2010	302.96	270.32

			(-) [3/2020]	(-) [302.96]	(0.00) [120]
1148	REORGANISATION OF BHARATPUR OCP EXPANSION	11/2018	3/2029 (-) [3/2029]	2,838.87 (-) [2,838.87]	1,169.40 (0.00) [0]
1149	SIARMAL OCP (40.00MTY)	5/2014	3/2026 (-) [3/2026]	3,756.36 (-) [3,756.36]	1,213.54 (0.00) [0]
	<u>Mines</u>				
1150	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/2014	4/2021 (12/2022) [12/2022]	5,540.00 (5,540.00) [5,540.00]	131.22 (0.00) [20]
1151	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	12/2015	11/2020 (-) [11/2020]	355.00 (-) [355.00]	85.98 (0.00) [0]
1152	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN	11/2017	4/2021 (4/2021) [4/2021]	483.00 (483.00) [483.00]	0.48 (0.00) [0]
1153	UTKAL D AND E COAL BLOCK	5/2016	1/2020 (-) [1/2020]	534.00 (-) [534.00]	320.63 (0.00) [0]
	<u>Petroleum</u>				
1154	2G ETHANOL BIO REFINERY AT BARGARH	8/2017	12/2020 (-) [12/2020]	750.00 (-) [750.00]	34.73 (0.00) [0]
1155	2ND GENERATION LIGNOCELLUOSIC BIOMASS ETHANOL BIOFUEL REFINERY AT BARGARH (ODISHA)	8/2019	8/2022 (-) [8/2022]	1,607.00 (-) [1,607.00]	40.99 (0.00) [0]
1156	ADDITIONAL STORAGE TANKS AT PARADIP	11/2018	9/2021 (-) [9/2021]	462.30 (-) [462.30]	0.00 (0.00) [0]
1157	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY	8/2017	12/2021 (-) [12/2020]	315.00 (-) [315.00]	124.98 (0.00) [-12]
1158	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR	7/2017	7/2022 (-) [7/2022]	243.53 (-) [243.53]	58.94 (0.00) [0]
1159	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK	7/2017	7/2022 (-) [7/2022]	182.20 (-) [182.20]	34.88 (0.00) [0]
1160	DHAMRA-ANGUL PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	1,933.00 (-) [1,933.00]	1,068.40 (0.00) [0]
1161	ETHYLENE GLYCOL PROJECT AT PARADIP	4/2018	10/2021 (-) [10/2021]	5,654.00 (-) [5,654.00]	686.68 (0.00) [0]
1162	Fuel Quality Upgradation Project at Paradip Refinery	5/2019	8/2021 (-) [8/2021]	3,361.00 (-) [3,361.00]	468.48 (0.00) [0]
1163	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY	5/2016	1/2019 (-) [6/2020]	429.00 (-) [429.00]	329.59 (0.00) [17]
1164	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY	6/2019	9/2022 (-) [9/2022]	371.00 (-) [371.00]	0.00 (0.00) [0]
1165	LPG BP PROJECT KHORDHA	12/2016	12/2019 (-) [7/2021]	161.59 (-) [161.59]	40.21 (0.00) [19]
1166	PARADIP SOMNATHPUR HALDIA PIPELINE	10/2018	10/2021 (-) [10/2021]	1,297.50 (-) [1,297.50]	30.00 (0.00) [0]

	Power				
1167	DARLIPALLI STPP STAGE-I (2X800 MW)	2/2014	12/2018 (2/2020) [8/2020]	12,532.44 (-) [13,740.53]	10,182.96 (1,208.09) [20]
1168	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL	5/2016	12/2018 (-) [8/2020]	1,885.13 (-) [1,885.13]	1,486.29 (0.00) [20]
	Railways				
1169	BANASPANI- JAKHPURA - DOUBLING	3/2009	3/2019 (-) [6/2022]	942.95 (-) [1,120.00]	1,046.08 (177.05) [39]
1170	BHADRAK - NERGUNDI 3RD LINE	3/2013	10/2020 (3/2023) [3/2023]	843.04 (843.04) [843.04]	147.39 (0.00) [29]
1171	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	4/2015	12/2018 (3/2022) [3/2023]	1,172.92 (1,172.92) [1,172.92]	560.36 (0.00) [51]
1172	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION	4/2010	3/2015 (-) [0/0]	149.90 (-) [230.00]	54.46 (80.10) [0]
1173	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL	4/2016	3/2020 (-) [6/2023]	5,200.00 (-) [1,700.43]	48.00 (-3,499.57) [39]
1174	HARIDASPUR-PARADEEP(NL)	4/1996	12/2017 (-) [3/2020]	1,185.64 (-) [1,844.47]	1,883.44 (658.83) [27]
1175	JAGADALPUR-KORAPUT DOUBLING	4/2015	3/2022 (3/2023) [3/2023]	1,547.38 (1,547.38) [1,547.38]	435.59 (0.00) [12]
1176	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	4/2015	11/2018 (-) [3/2022]	701.61 (701.61) [810.02]	139.27 (108.41) [40]
1177	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	4/2000	3/2009 (3/2009) [6/2020]	133.41 (207.00) [396.00]	388.21 (262.59) [135]
1178	KHURDA ROAD-BOLANGIR(NL)ECOR	4/1994	3/2009 (-) [6/2024]	2,923.13 (3,791.66) [3,791.66]	1,270.24 (868.53) [183]
1179	KORAPUT - SINGAPUR ROAD DOUBLING	4/2015	3/2022 (-) [3/2025]	2,361.74 (2,361.74) [2,361.74]	247.79 (0.00) [36]
1180	ROURKELA JHARSUGUDA THIRD LINE 101 KM	11/2015	3/2020 (3/2020) [3/2021]	969.83 (1,312.96) [1,312.96]	610.19 (343.13) [12]
1181	SAMBALPUR - ANGUL RLY. ELECTRIFICATION	3/2012	3/2020 (-) [3/2021]	155.81 (-) [238.03]	205.65 (82.22) [12]
1182	SAMBALPUR - TITLAGARH - DOUBLING	3/2006	3/2020 (-) [3/2021]	948.04 (-) [1,500.00]	1,451.81 (551.96) [12]
1183	SAMBALPUR-TALCHER DOUBLING	3/2011	2/2019 (3/2022) [3/2022]	1,111.99 (1,539.28) [1,539.28]	972.93 (427.29) [37]
1184	SUKINDA ROAD - ANGUL (NL)(ECOR)	4/1998	2/2015 (-) [12/2021]	1,202.70 (-) [1,202.70]	1,008.33 (0.00) [82]
1185	TALCHER-BIMALAGARH(NL)(ECOR)	4/2005	6/2021 (-) [6/2024]	810.78 (198.07) [1,928.07]	780.24 (1,117.29) [36]
1186	VIZIANAGARAM -SAMABALPUR 3RD LINE	1/1991	12/2024 (-)	2,335.67 (-)	698.45 (0.01)

			[12/2024]	[2,335.68]	[0]
	Road Transport And Highways				
1187	4 LANING OF BAHARAGORA - SINGHARA	7/2015	/	1,282.94	288.42
			(-)	(-)	(0.00)
			[3/2021]	[1,282.94]	[-]
1188	DEVELOPMENT OF FOUR LANNING OF ANGUL- SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S	9/2016	8/2019	2,510.04	358.51
			(-)	(-)	(0.00)
			[3/2021]	[2,510.04]	[19]
1189	FOUR LANING WITH PS TALEBANI -SMBALPUR	12/2015	/	752.28	76.78
			(-)	(-)	(0.00)
			[0/0]	[752.28]	[0]
1190	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION	2/2016	/	1,069.65	546.51
			(-)	(-)	(0.00)
			[3/2020]	[1,069.65]	[-]
1191	PANIKHOLI-RIMOLI	3/2012	9/2014	1,410.00	1,935.14
			(-)	(-)	(0.00)
			[0/0]	[1,410.00]	[0]
1192	REHABILITAITON AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4	10/2016	/	1,008.96	595.10
			(-)	(-)	(0.00)
			[3/2021]	[1,008.96]	[-]
1193	REHABILITATION AND UP GRADATION OF EXISTING 2- LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS	1/2018	/	564.66	89.77
			(-)	(-)	(0.00)
			[8/2021]	[564.66]	[-]
1194	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	7/2017	7/2017	476.56	1.49
			(11/2020)	(-)	(0.00)
			[6/2021]	[476.56]	[47]
1195	REHABILITATION AND UP-GRADATION OF EXISTING 2- LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (	1/2018	/	633.68	0.00
			(-)	(-)	(0.00)
			[0/0]	[633.68]	[0]
1196	REHABILITATION AND UP-GRADATION OF EXISTING 2- LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25	1/2018	/	953.09	224.11
			(5/2020)	(-)	(0.00)
			[6/2021]	[953.09]	[-]
1197	REHABILITATION AND UP-GRADATION OF EXISTING 2- LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2	1/2018	/	668.86	175.29
			(5/2020)	(-)	(0.00)
			[6/2021]	[668.86]	[-]
1198	REHABILITATION AND UP-GRADATION OF EXISTING 2- LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG	1/2018	/	614.48	93.00
			(-)	(-)	(0.00)
			[8/2021]	[614.48]	[-]
1199	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH	7/2014	1/2017	342.05	258.91
			(-)	(-)	(0.00)
			[0/0]	[342.05]	[0]
1200	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (	1/2018	/	503.88	8.84
			(-)	(-)	(0.00)
			[6/2021]	[503.88]	[-]
1201	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	3/2017	3/2020	1,288.07	532.31
			(-)	(-)	(131.93)
			[3/2021]	[1,420.00]	[12]
1202	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO	12/2017	/	686.65	114.36
			(7/2020)	(-)	(0.00)
			[6/2021]	[686.65]	[-]
1203	REHABILITATION AND UPGRADATION OF CUTTACK- ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON	1/2018	/	686.65	105.69
			(3/2020)	(-)	(0.00)
			[6/2021]	[686.65]	[-]
1204	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA	12/2017	/	417.51	44.14
			(-)	(-)	(0.00)
			[6/2021]	[417.51]	[-]
1205	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN	7/2014	1/2017	342.05	258.91
			(-)	(342.00)	(-0.05)
			[0/0]	[342.00]	[0]
1206	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM	1/2018	/	999.00	0.00
			(-)	(-)	(0.00)

	199.141		[6/2021]	[999.00]	[-]
1207	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR	8/2013	6/2016 (-) [0/0]	171.96 (172.00) [172.00]	88.30 (0.04) [0]
1208	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB	1/1991	10/2017 (-) [0/0]	218.63 (-) [218.63]	29.27 (0.00) [0]
1209	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK	1/1991	5/2018 (-) [0/0]	229.41 (-) [229.41]	6.65 (0.00) [0]
1210	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK	1/2018	/ (6/2021) [6/2021]	1,522.00 (-) [1,522.00]	243.52 (0.00) [-]
1211	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	12/2011	6/2014 (-) [3/2019]	1,047.00 (-) [1,047.00]	1,874.43 (0.00) [0]
1212	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000)	3/2018	/ (-) [4/2021]	806.11 (-) [806.11]	21.39 (0.00) [-]
1213	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO	3/2014	5/2016 (-) [0/0]	191.50 (192.00) [192.00]	136.19 (0.50) [0]
1214	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM	2/2015	10/2017 (-) [0/0]	239.91 (240.00) [160.00]	147.25 (-79.91) [0]
1215	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W	1/2015	4/2018 (-) [0/0]	326.63 (327.00) [326.63]	249.26 (0.00) [0]
1216	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG	6/2016	6/2018 (-) [0/0]	157.30 (157.00) [157.30]	97.29 (0.00) [0]
1217	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA	12/2011	11/2017 (-) [0/0]	159.39 (-) [159.39]	210.29 (0.00) [0]
1218	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA	12/2011	8/2015 (-) [0/0]	191.08 (-) [191.08]	99.98 (0.00) [0]
1219	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA.	8/2016	2/2017 (-) [0/0]	287.70 (-) [287.70]	153.90 (0.00) [0]
1220	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA	3/2018	8/2018 (-) [0/0]	214.23 (-) [214.23]	23.44 (0.00) [0]
1221	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26.	3/2016	12/2016 (-) [0/0]	165.06 (-) [165.06]	92.59 (0.00) [0]
1222	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA	12/2016	8/2018 (-) [0/0]	223.50 (-) [223.50]	44.52 (0.00) [0]
1223	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA	3/2018	8/2018 (-) [0/0]	199.16 (-) [199.16]	25.63 (0.00) [0]
1224	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA	9/2016	2/2017 (-) [0/0]	295.67 (-) [295.67]	127.75 (0.00) [0]
1225	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA	12/2016	4/2018 (-) [0/0]	206.88 (-) [206.88]	41.69 (0.00) [0]
	Steel				
1226	INSTALLATION OF NEW HOT STRIP MILL AT RSP	4/2015	4/2018 (1/2020)	3,127.30 (-)	3,201.42 (0.00)

			[1/2020]	[3,127.30]	[21]
	<u>Urban Development</u>				
1227	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR	1/2019	3/2022 (6/2022) [6/2022]	790.79 (-) [790.79]	41.06 (0.00) [3]
	<u>PONDICHERRY</u>				
1228	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT	3/2018	9/2020 (-) [1/2021]	195.00 (-) [195.00]	0.00 (0.00) [4]
	<u>PUNJAB</u>				
	<u>Fertilisers</u>				
1229	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA	1/2018	11/2019 (-) [5/2020]	218.83 (-) [218.83]	142.01 (0.00) [6]
1230	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL	1/2018	11/2019 (-) [5/2020]	239.81 (-) [239.81]	156.70 (0.00) [6]
	<u>Health And Family Welfare</u>				
1231	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	7/2016	6/2020 (-) [10/2020]	703.00 (-) [557.48]	327.76 (-145.52) [4]
1232	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	7/2016	2/2018 (-) [3/2020]	152.95 (-) [177.92]	147.31 (24.97) [25]
	<u>Railways</u>				
1233	QADIAN-BEAS	4/2011	/ (-) [3/2024]	205.22 (-) [841.90]	1.73 (636.68) [-]
	<u>Road Transport And Highways</u>				
1234	4 LANING FROM PHAGWARA TO RUPNAGAR	8/2016	/ (-) [4/2020]	1,169.61 (1,367.00) [1,169.61]	1,203.12 (0.00) [-]
1235	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600	11/2015	/ (12/2019) [0/0]	847.02 (-) [847.02]	795.00 (0.00) [0]
1236	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00	11/2015	/ (5/2020) [0/0]	889.24 (904.82) [904.82]	739.41 (15.58) [0]
1237	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	8/2016	9/2019 (3/2020) [3/2020]	1,388.34 (2,541.32) [2,587.50]	1,449.00 (1,199.16) [6]
1238	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN	3/2017	3/2020 (-) [8/2021]	754.54 (-) [756.27]	193.96 (1.73) [17]
1239	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS	12/2015	/ (9/2019) [0/0]	766.36 (-) [766.36]	685.36 (0.00) [0]
1240	FOUR LANING OF CHANDIGARH - KHARAR	10/2015	12/2017 (6/2020) [6/2020]	447.29 (746.43) [746.43]	614.07 (299.14) [30]
1241	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB	2/2018	/ (-) [1/2021]	261.76 (-) [207.00]	112.77 (-54.76) [-]
1242	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION	9/2014	/ (-) [6/2020]	479.00 (-) [479.00]	453.80 (0.00) [-]
1243	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200	10/2017	10/2019 (12/2020) [12/2020]	1,069.59 (-) [1,069.59]	663.50 (0.00) [14]
1244	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START	3/2018	/ (-)	196.05 (149.90)	143.03 (0.00)

	OF AMRI		[1/2020]	[196.05]	[-]
1245	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN	3/2018	/ (-) [0/0]	199.90 (149.90) [199.90]	112.43 (0.00) [0]
1246	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0.000	3/2018	11/2020 (-) [5/2021]	170.57 (192.48) [170.57]	8.14 (0.00) [6]
1247	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF	3/2018	6/2020 (-) [6/2020]	173.24 (-) [173.24]	56.66 (0.00) [0]
1248	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH	3/2018	7/2020 (-) [7/2020]	322.48 (-) [322.48]	153.18 (0.00) [0]
1249	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES	3/2018	8/2020 (-) [8/2020]	293.64 (-) [293.64]	28.24 (0.00) [0]
1250	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES	3/2018	8/2020 (-) [8/2020]	293.64 (-) [293.64]	134.32 (0.00) [0]
1251	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA	3/2018	8/2020 (-) [8/2020]	293.10 (-) [293.10]	63.14 (0.00) [0]
1252	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA	6/2015	/ (2/2018) [0/0]	892.17 (-) [892.17]	648.44 (0.00) [0]
	<u>Urban Development</u>				
1253	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	2/2014	5/2017 (-) [3/2020]	388.00 (500.18) [490.00]	442.51 (102.00) [34]
1254	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	1/2018	5/2020 (-) [2/2021]	430.00 (387.83) [387.83]	124.24 (-42.17) [9]
1255	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	8/2016	4/2019 (-) [5/2020]	294.00 (350.69) [350.69]	219.60 (56.69) [13]
	<u>RAJASTHAN</u>				
	<u>Atomic Energy</u>				
1256	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016 (-) [3/2023]	12,320.00 (-) [17,079.00]	11,737.00 (4,759.00) [75]
	<u>Coal</u>				
1257	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	3/2015	12/2019 (-) [0/0]	513.63 (-) [513.63]	175.30 (0.00) [0]
1258	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	3/2015	9/2019 (-) [0/0]	522.45 (-) [522.45]	9.88 (0.00) [0]
	<u>Petroleum</u>				
1259	LPG BP PROJECT JODHPUR	3/2018	/ (-) [3/2021]	229.80 (-) [229.80]	74.47 (0.00) [-]
	<u>Railways</u>				
1260	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	5/2015	/ (-) [0/0]	873.71 (-) [1,980.21]	4.60 (1,106.50) [0]
1261	AJMER-BANGURGRAM	4/2011	11/2019 (-) [12/2020]	213.39 (-) [303.56]	285.01 (90.17) [13]
1262	AJMER-KOTA (NASIRABAD-JAUNDRI)	4/2013	/ (-) [0/0]	822.00 (-) [1,099.54]	0.00 (277.54) [0]

1263	ALWAR-BANDIKUI DOUBLING	4/2013	2/2019 (-) [2/2020]	242.09 (281.03) [410.00]	381.92 (167.91) [12]
1264	BANGURGRAM-GURIYA PATCH DOUBLING	4/2012	12/2019 (-) [2/2021]	246.08 (-) [348.55]	248.71 (102.47) [14]
1265	DAUSA-GANGAPUR CITY(NL),NWR	2/1997	2/2019 (-) [6/2021]	410.08 (780.98) [886.41]	568.73 (476.33) [28]
1266	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM)	8/2018	8/2022 (-) [9/2022]	808.85 (-) [808.85]	81.26 (0.00) [1]
1267	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR	4/2013	3/2020 (-) [12/2020]	420.18 (-) [420.18]	199.53 (0.00) [9]
1268	MULTI MODAL LOGISTICS PARK AT KATHUWAS	1/2011	3/2018 (-) [3/2020]	493.17 (-) [493.17]	443.19 (0.00) [24]
1269	PUSHKAR-MERTA	4/2013	/ (-) [0/0]	323.00 (-) [432.22]	0.00 (109.22) [0]
1270	THIYAT HAMIRA-SANU	4/2013	10/2018 (-) [12/2019]	236.93 (-) [350.45]	232.02 (113.52) [0]
	<u>Road Transport And Highways</u>				
1271	2 LANING WITH PS OF GULABPURA - UNIARA	10/2015	10/2017 (-) [3/2020]	597.00 (-) [597.00]	587.64 (0.00) [29]
1272	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR	8/2016	1/2019 (-) [0/0]	320.30 (-) [320.30]	237.81 (0.00) [0]
1273	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA	11/2012	8/2016 (-) [6/2020]	530.07 (-) [530.07]	556.02 (0.00) [46]
1274	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A	7/2016	/ (5/2017) [2/2020]	688.70 (881.00) [688.70]	870.48 (0.00) [-]
1275	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE-	12/2016	/ (-) [8/2020]	1,031.95 (-) [1,031.95]	367.00 (0.00) [-]
1276	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN.	3/2019	/ (-) [0/0]	178.13 (-) [178.13]	25.21 (0.00) [0]
1277	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM	8/2014	4/2018 (-) [0/0]	822.90 (-) [822.90]	844.08 (0.00) [0]
1278	CITTORGARH-NEEMACH (4L) OF NH-79 AND NIMBAHARA PRATAPGARH (2L+PS) OF NH-113 UNDER PPP.	10/2012	10/2013 (-) [0/0]	511.21 (-) [511.21]	814.79 (0.00) [0]
1279	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM	3/2018	/ (-) [0/0]	1,158.35 (-) [1,158.35]	496.04 (0.00) [0]
1280	CONSTRUCTION OF 4 LANING BY CC PAVEMENT ON KOTA-DARAH OF NH-12 FROM 256/550 TO 289/550 UNDER EPC.	12/2015	10/2016 (-) [0/0]	621.43 (-) [621.43]	427.45 (0.00) [0]
1281	CONSTRUCTION OF NAGAU BYPASS FROM EXISTING KM 166/260 TO KM 180/500 OF NH-65 ON EPC MODE.	3/2016	9/2016 (-) [0/0]	155.77 (-) [155.77]	110.34 (0.00) [0]
1282	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709	11/2017	4/2018 (-) [0/0]	163.95 (-) [163.95]	128.05 (0.00) [0]

1283	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH.	2/2018	/ (-) [0/0]	716.76 (-) [716.76]	283.46 (0.00) [0]
1284	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA	2/2018	/ (-) [0/0]	741.86 (-) [741.86]	0.00 (0.00) [0]
1285	DEVELOPMENT AND OPERATION OF BIKANER-SURATGARH SECTION OF NH-15 BY 2L+PS IN THE STATE OF RAJASTHAN	3/2009	9/2013 (-) [0/0]	501.00 (671.54) [671.54]	659.98 (170.54) [0]
1286	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO	12/2017	/ (-) [12/2020]	1,308.73 (-) [1,308.73]	99.68 (0.00) [-]
1287	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM	6/2016	6/2019 (-) [11/2019]	763.23 (-) [763.23]	439.88 (0.00) [0]
1288	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM	6/2016	6/2019 (-) [9/2019]	649.00 (-) [649.00]	322.84 (0.00) [0]
1289	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540	10/2017	10/2017 (-) [11/2020]	964.17 (-) [964.17]	390.91 (0.00) [37]
1290	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	2/2008	10/2011 (-) [0/0]	1,673.70 (-) [1,673.70]	3,326.93 (0.00) [0]
1291	NAGAU-BIKANER OF NH-11 (2L+PS) UNDER PPP.	1/2012	1/2014 (-) [0/0]	378.07 (478.73) [478.73]	188.98 (100.66) [0]
1292	NETRA VILLAGE TO MANDORE SECTION OF NH-65 KM 267+500 TO 296+070 (4L) UNDER EPC.	10/2014	1/2015 (-) [0/0]	382.81 (-) [382.81]	335.93 (0.00) [0]
1293	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING	9/2012	10/2013 (-) [0/0]	511.00 (-) [511.00]	492.00 (0.00) [0]
1294	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A	9/2012	10/2013 (-) [0/0]	511.00 (-) [511.00]	2,323.04 (0.00) [0]
1295	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS	10/2013	5/2014 (-) [0/0]	278.87 (-) [278.87]	0.00 (0.00) [0]
1296	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O	1/1991	4/2014 (-) [0/0]	376.52 (-) [376.52]	0.00 (0.00) [0]
1297	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I	9/2016	/ (-) [5/2020]	1,100.19 (-) [1,145.31]	1,045.00 (45.12) [-]
1298	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (	9/2016	/ (-) [5/2020]	1,239.82 (-) [1,239.82]	1,427.14 (0.00) [-]
1299	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV	4/2017	4/2020 (-) [4/2020]	894.00 (-) [929.32]	760.00 (35.32) [0]
1300	TWO LANING WITH PAVED SHOULDER OF KARAUII - DHOLPUR	9/2014	9/2016 (9/2014) [10/2019]	425.19 (-) [425.19]	276.40 (0.00) [0]
1301	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR	8/2015	/ (2/2016) [10/2019]	275.90 (-) [275.90]	289.13 (0.00) [0]
1302	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM	7/2016	10/2018 (-) [0/0]	331.46 (-) [331.46]	267.94 (0.00) [0]
1303	TWO LANNING WITH PAVED SHOULDER OF SALASAR-	6/2016	6/2019	637.18	550.35

	NAGPUR		(-) [9/2019]	(-) [637.18]	(0.00) [0]
1304	UP-GRADATION TO 2 LANE WITH PAVED SHOULDER FOR SECTION FROM KM 118.900 TO KM 156.955 BALOTRA TOSANDE	1/2017	7/2017 (-) [0/0]	163.54 (-) [163.54]	106.25 (0.00) [0]
1305	UP-GRADATION TO TWO LANE WITH PAVED SHOULDER FOR SECTION FROM KM 58.000 TO KM 91.600 (BALOTRA TO SAN	1/2017	11/2017 (-) [0/0]	179.32 (-) [179.32]	120.78 (0.00) [0]
1306	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE - DANTOUR-JA	3/2018	/ (-) [0/0]	874.25 (-) [874.25]	288.37 (0.00) [0]
1307	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM-	2/2018	6/2018 (-) [0/0]	370.30 (-) [370.30]	207.58 (0.00) [0]
1308	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION	2/2018	/ (-) [9/2020]	1,103.88 (-) [1,103.88]	404.43 (0.00) [-]
1309	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM-	2/2018	5/2018 (-) [0/0]	341.79 (-) [341.79]	299.48 (0.00) [0]
1310	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING	10/2014	1/2015 (-) [0/0]	257.09 (-) [257.09]	14.18 (0.00) [0]
1311	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24	2/2015	3/2015 (-) [0/0]	383.40 (-) [383.40]	244.68 (0.00) [0]
1312	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K	10/2014	1/2015 (-) [0/0]	269.22 (-) [269.22]	33.24 (0.00) [0]
1313	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH	12/2015	6/2018 (-) [0/0]	621.43 (-) [621.43]	387.22 (0.00) [0]
1314	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR	11/2017	4/2018 (-) [0/0]	187.82 (-) [187.82]	95.15 (0.00) [0]
	Urban Development				
1315	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS	5/2015	3/2017 (-) [0/0]	189.00 (-) [189.00]	0.00 (0.00) [0]
1316	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	12/2016	7/2019 (3/2020) [8/2020]	549.31 (559.47) [559.47]	373.45 (10.16) [13]
	SIKKIM				
	Railways				
1317	SEVOK RANGPO, NEFR	4/2008	12/2015 (-) [0/0]	1,339.48 (-) [4,084.69]	332.23 (2,745.21) [0]
	Road Transport And Highways				
1318	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	1/2013	2/2013 (-) [12/2019]	182.28 (-) [269.14]	185.49 (86.86) [0]
1319	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	4/2013	8/2013 (-) [12/2019]	151.59 (240.58) [151.59]	196.76 (0.00) [0]
1320	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM.	4/2013	8/2013 (-) [0/0]	166.27 (-) [166.27]	141.31 (0.00) [0]
1321	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	3/2017	/ (-) [0/0]	375.80 (-) [375.80]	77.39 (0.00) [0]
1322	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER	11/2017	11/2017	290.05	54.13

	INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5		(-) [0/0]	(-) [290.05]	(0.00) [0]
1323	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA	4/2017	11/2017 (-) [0/0]	318.42 (-) [318.42]	66.63 (0.00) [0]
1324	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	3/2018	6/2018 (-) [0/0]	264.84 (-) [264.84]	0.00 (0.00) [0]
1325	RHENOK-RORATHANG-PAKYONG ON NH 717A	4/2017	10/2017 (-) [0/0]	388.00 (-) [447.37]	155.85 (59.37) [0]
	<u>TAMIL NADU</u>				
	<u>Atomic Energy</u>				
1326	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	3/2013	11/2020 (-) [11/2023]	39,849.00 (-) [39,849.00]	17,987.00 (0.00) [36]
1327	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	9/2003	9/2010 (9/2016) [10/2021]	3,492.00 (5,677.00) [6,840.00]	5,862.38 (3,348.00) [133]
	<u>Civil Aviation</u>				
1328	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	6/2018	2/2022 (-) [8/2022]	2,467.00 (-) [2,467.00]	213.17 (0.00) [6]
1329	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI	8/2018	10/2021 (-) [10/2021]	951.28 (-) [951.28]	71.55 (0.00) [0]
	<u>Coal</u>				
1330	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	4/2013	6/2015 (-) [0/0]	1,458.17 (709.06) [709.06]	462.63 (-749.11) [0]
1331	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	6/2011	12/2015 (-) [3/2020]	5,907.11 (7,080.41) [7,080.41]	6,954.15 (1,173.30) [51]
	<u>Mines</u>				
1332	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU	9/2017	6/2019 (12/2020) [12/2020]	166.62 (163.17) [163.17]	135.00 (-3.45) [18]
	<u>Petroleum</u>				
1333	AUGMENTATION OF CTMPL	12/2016	6/2020 (-) [6/2020]	228.00 (-) [228.00]	36.09 (0.00) [0]
1334	BS-VI PROJECTS	9/2017	12/2019 (-) [4/2020]	1,858.00 (-) [1,858.00]	1,229.51 (0.00) [4]
1335	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	12/2017	10/2020 (-) [8/2021]	466.43 (-) [466.43]	68.41 (0.00) [10]
1336	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	5/2016	12/2018 (-) [2/2021]	4,497.00 (6,025.00) [6,025.00]	1,588.02 (1,528.00) [26]
1337	ENNORE-TRICHY-MADURAI LPG PIPELINE	5/2013	6/2020 (-) [6/2020]	711.00 (-) [711.00]	11.12 (0.00) [0]
1338	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	11/2015	3/2019 (5/2020) [5/2020]	650.82 (-) [650.82]	432.28 (0.00) [14]
1339	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	2/2017 (-) [10/2021]	678.00 (-) [678.00]	8.10 (0.00) [56]
1340	RE-LIQUIFIED NATURAL GAS	8/2017	8/2020 (-)	421.00 (-)	177.80 (0.00)

			[2/2021]	[421.00]	[6]
1341	RESID UPGRADATION PROJECT	3/2013	11/2015 (-) [0/0]	3,110.36 (-) [3,110.36]	2,915.00 (0.00) [0]
	<u>Power</u>				
1342	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY	5/2017	7/2019 (-) [3/2020]	186.17 (-) [186.17]	111.47 (0.00) [8]
	<u>Railways</u>				
1343	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING	2/1999	3/2018 (-) [0/0]	257.00 (257.00) [257.00]	268.31 (0.00) [0]
1344	ATTIPPATTU PUTTUR	4/2008	2/2019 (-) [0/0]	151.84 (-) [1,105.00]	3.34 (953.16) [0]
1345	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	4/2007	/ (-) [3/2020]	931.98 (-) [951.24]	753.41 (19.26) [-]
1346	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	4/1999	/ (-) [0/0]	198.68 (-) [556.64]	305.22 (357.96) [0]
1347	ERODE-PALANI	4/2008	/ (-) [0/0]	288.57 (-) [1,140.00]	1.63 (851.43) [0]
1348	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	4/2006	6/2013 (-) [0/0]	495.74 (-) [734.01]	445.91 (238.27) [0]
1349	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	2/2015	3/2020 (-) [6/2021]	760.00 (-) [1,182.31]	446.00 (422.31) [15]
1350	MADURAI-BODINAYAKKANUR	4/2008	/ (-) [3/2020]	164.41 (-) [450.00]	197.11 (285.59) [-]
1351	MANIYACHI - NAGERCOIL (102 KM) DOUBLING	2/2015	3/2022 (-) [3/2022]	1,700.00 (-) [1,003.00]	252.02 (-697.00) [0]
1352	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	9/2007	2/2019 (-) [2/2020]	724.69 (-) [2,072.50]	1,471.60 (1,347.81) [12]
1353	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM	10/2013	4/2014 (-) [3/2020]	187.26 (-) [231.67]	167.12 (44.41) [71]
1354	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	4/2013	/ (-) [0/0]	839.00 (-) [1,500.00]	0.62 (661.00) [0]
1355	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	2/1996	3/2005 (-) [0/0]	268.87 (-) [950.00]	927.86 (681.13) [0]
1356	TIDIVANAM-NAGARI (NL)	9/2006	/ (-) [0/0]	582.83 (-) [2,300.00]	243.44 (1,717.17) [0]
1357	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	9/2006	/ (-) [0/0]	227.40 (-) [900.00]	63.28 (672.60) [0]
1358	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	9/1995	3/2020 (-) [3/2021]	303.98 (-) [980.00]	683.11 (676.02) [12]
1359	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM)	2/2017	3/2024 (-) [3/2026]	1,567.00 (-) [1,567.00]	0.00 (0.00) [24]
	<u>Road Transport And Highways</u>				

1360	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI	9/2011	8/2013 (-) [0/0]	485.00 (-) [485.00]	406.68 (0.00) [0]
1361	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHHTH 170 KM)	4/2012	4/2014 (-) [0/0]	624.00 (-) [624.00]	350.79 (0.00) [0]
1362	4-LANNING OF OTTANCHATRAM BYPASS	9/2017	9/2017 (-) [4/2020]	244.27 (-) [244.27]	177.41 (0.00) [31]
1363	4-LANNING OF STHIYATHOPU-CHOLOPURAM	9/2017	9/2017 (-) [8/2020]	1,227.87 (-) [1,227.87]	387.40 (0.00) [35]
1364	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT	3/2015	8/2015 (-) [0/0]	258.97 (-) [268.92]	0.00 (9.95) [0]
1365	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I-	11/2015	8/2015 (-) [0/0]	154.14 (-) [154.14]	0.00 (0.00) [0]
1366	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	6/2011	6/2013 (1/2019) [8/2020]	600.00 (-) [600.00]	329.92 (0.00) [86]
1367	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS	3/2018	/ (-) [4/2021]	1,016.92 (-) [1,071.00]	0.00 (54.08) [-]
1368	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120	5/2015	11/2017 (-) [7/2019]	1,387.11 (-) [1,387.11]	980.46 (0.00) [0]
1369	FOUR LANING OF MADURAI- CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICKULAM (7/300)	3/2018	/ (-) [11/2020]	628.71 (-) [628.71]	120.55 (0.00) [-]
1370	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N	3/2018	/ (-) [0/0]	2,065.96 (-) [2,169.00]	0.00 (103.04) [0]
1371	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU	2/2018	/ (-) [2/2021]	1,166.26 (-) [1,166.26]	163.29 (0.00) [-]
1372	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	3/2016	7/2016 (-) [5/2020]	641.17 (-) [641.17]	370.82 (0.00) [46]
1373	FOUR LANING OF CHETTICKULAM TO NATHAM SECTION OF NH-785 FROM CHETTICKULUM (KM 7.300) TO NATHAM (KM. 3	3/2018	/ (-) [11/2020]	505.35 (-) [505.35]	100.44 (0.00) [-]
1374	FOUR LANNING OF CHOLOPURAM-THANJAVUR	8/2017	8/2017 (-) [9/2020]	1,176.37 (-) [1,176.37]	207.17 (0.00) [37]
1375	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH	2/2016	8/2018 (-) [3/2020]	707.82 (-) [707.82]	381.40 (0.00) [19]
1376	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65.	3/2017	3/2020 (-) [3/2020]	848.45 (-) [848.45]	103.14 (0.00) [0]
1377	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K	2/2016	7/2018 (-) [5/2020]	641.17 (-) [641.17]	370.82 (0.00) [22]
1378	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO	3/2015	7/2015 (-) [0/0]	157.18 (162.00) [162.00]	0.00 (4.82) [0]
1379	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE	12/2017	/ (-) [3/2020]	379.90 (-) [379.90]	125.68 (0.00) [-]
1380	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION	9/2011	12/2013	1,250.00	1,336.07

	KM.0.00 TO KM.148.3 NH-46		(-) [6/2020]	(-) [1,250.00]	(0.00) [78]
1381	THIRUMAYAM - MANAMADURAI SECTION	7/2014	1/2017 (-) [0/0]	401.11 (-) [401.11]	273.89 (0.00) [0]
1382	TRICHY - KARUR	3/2007	7/2008 (-) [0/0]	516.00 (-) [516.00]	886.96 (0.00) [0]
1383	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS	5/2010	5/2013 (-) [0/0]	374.00 (-) [374.00]	237.00 (0.00) [0]
1384	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N	3/2018	/ (-) [0/0]	633.55 (-) [482.04]	0.00 (-151.51) [0]
1385	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	6/2015	12/2017 (-) [0/0]	563.92 (-) [563.92]	93.53 (0.00) [0]
	<u>Urban Development</u>				
1386	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	12/2015	10/2019 (-) [7/2020]	209.00 (-) [209.00]	150.71 (0.00) [9]
1387	CHENNAI METRO RAIL LTD (PHASE 1 EXT)	6/2016	3/2018 (6/2020) [6/2020]	3,770.00 (-) [3,770.00]	2,258.91 (0.00) [27]
1388	CHENNAI METRO RAIL LTD (PHASE 1)	2/2009	12/2015 (-) [0/0]	14,600.00 (-) [19,058.00]	16,352.87 (4,458.00) [0]
1389	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI	11/2017	/ (-) [11/2021]	348.77 (-) [348.77]	31.98 (0.00) [-]
	<u>TELANGANA</u>				
	<u>Coal</u>				
1390	KALYANIKHANI 6 INCLINE PROJECT	12/2015	3/2020 (-) [3/2020]	477.65 (-) [477.65]	2.11 (0.00) [0]
1391	KOYAGUDEM OPENCAST PROJECT	10/2015	3/2018 (-) [3/2020]	426.79 (-) [426.79]	0.72 (0.00) [24]
1392	JALAGAM VENGALA RAO OCP-II	7/2011	3/2015 (-) [3/2021]	447.06 (-) [473.22]	18.60 (26.16) [72]
1393	KAKATIYA LONGWALL	12/2008	12/2012 (-) [0/0]	453.63 (-) [453.63]	121.91 (0.00) [0]
1394	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1	3/2017	3/2019 (-) [3/2022]	413.84 (-) [413.84]	123.18 (0.00) [36]
1395	KAKATIYAKHANI OPENCAST-2 PROJECT	5/2015	3/2019 (-) [3/2020]	397.09 (-) [442.42]	99.56 (45.33) [12]
1396	KALYANIKHANI OPENCAST PROJECT	7/2012	7/2016 (-) [3/2020]	417.33 (-) [384.32]	115.04 (-33.01) [44]
1397	KISTARAM OCP	11/2010	3/2015 (-) [3/2021]	242.29 (-) [164.04]	120.31 (-78.25) [72]
1398	MANUGURU OC-II EXTENSION PHASE-II	3/2010	3/2012 (-) [0/0]	181.19 (-) [181.19]	170.60 (0.00) [0]
1399	RAMAGUNDAM OC-II EXTENSION	12/2009	3/2012 (-)	418.97 (-)	416.88 (70.65)

			[3/2023]	[489.62]	[132]
1400	RAMPURAM SHAFT BLOCK	8/2016	/	431.92	0.00
			(3/2023)	(-)	(0.00)
			[0/0]	[431.92]	[0]
1401	RCE OF INDARAM OCP(1.20 MTPA)	7/2011	3/2015	162.76	12.27
			(-)	(-)	(186.52)
			[3/2021]	[349.28]	[72]
1402	RFR OF MANUGURU OC PROJECT	11/2012	3/2016	430.45	189.54
			(-)	(-)	(-15.08)
			[3/2020]	[415.37]	[48]
1403	RG OC -III EXTENSION (PHASE -II) PROJECT	6/2012	6/2015	365.01	171.06
			(-)	(-)	(0.00)
			[3/2020]	[365.01]	[57]
1404	RKP OCP PHASE-I	3/2010	3/2015	209.78	137.06
			(-)	(-)	(0.00)
			[3/2020]	[209.78]	[60]
1405	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	3/2012	249.03	326.69
			(-)	(-)	(199.83)
			[3/2024]	[448.86]	[144]
1406	SRAVANAPALLI OPENCAST PROJECT	2/2018	/	412.70	0.76
			(3/2023)	(-)	(0.00)
			[0/0]	[412.70]	[0]
1407	SRP OC-II EXPANSION PROJECT	11/2016	/	272.73	153.75
			(4/2017)	(-)	(0.00)
			[3/2020]	[272.73]	[-]
	<u>Petroleum</u>				
1408	GRASS ROOT TERMINAL AT MALKAPUR	12/2018	4/2022	611.00	13.32
			(-)	(-)	(0.00)
			[3/2023]	[611.00]	[11]
	<u>Power</u>				
1409	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	1/2016	11/2020	10,598.98	6,325.54
			(2/2021)	(-)	(0.00)
			[9/2021]	[10,598.98]	[10]
	<u>Railways</u>				
1410	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	4/2012	3/2016	632.68	720.70
			(-)	(-)	(183.87)
			[12/2020]	[816.55]	[57]
1411	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY	3/2015	3/2021	636.38	392.54
			(-)	(-)	(0.00)
			[3/2021]	[636.38]	[0]
1412	MACHERLA-NALGONDA(NL)(SCR)	7/1998	/	458.25	3.83
			(-)	(458.25)	(0.01)
			[0/0]	[458.26]	[0]
1413	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	4/2017	3/2022	119.73	298.13
			(-)	(176.17)	(329.66)
			[12/2022]	[449.39]	[9]
1414	MANOHARABAD-KOTHPALL NEW LINE(SCR)	4/2006	3/2010	1,160.48	340.48
			(-)	(1,160.48)	(0.00)
			[3/2023]	[1,160.48]	[156]
1415	MANUGURU-RAMAGUNDAM	4/2013	/	1,112.00	0.92
			(-)	(2,911.84)	(1,799.84)
			[0/0]	[2,911.84]	[0]
1416	SECUNDERABAD-MAHABUBNAGAR DOUBLING	4/2015	12/2024	773.94	556.16
			(-)	(-)	(0.00)
			[12/2024]	[773.94]	[0]
	<u>Road Transport And Highways</u>				
1417	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	4/2014	9/2016	1,266.60	1,446.45
			(-)	(-)	(277.40)
			[0/0]	[1,544.00]	[0]
1418	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD	1/2018	5/2020	283.15	42.22
			(-)	(-)	(0.00)

	SECTION OF NH		[5/2020]	[283.15]	[0]
1419	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES	3/2018	7/2020 (-) [7/2020]	626.76 (-) [626.76]	80.66 (0.00) [0]
1420	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM	3/2015	1/2017 (-) [0/0]	153.21 (-) [153.21]	100.10 (0.00) [0]
1421	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB	3/2017	3/2017 (-) [0/0]	4,429.00 (-) [4,429.00]	0.00 (0.00) [0]
1422	FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3	3/2018	/ (-) [0/0]	857.62 (-) [857.62]	4.89 (0.00) [0]
1423	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K	3/2018	/ (-) [0/0]	802.65 (-) [802.65]	91.76 (0.00) [0]
1424	FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM	3/2018	/ (-) [0/0]	950.63 (-) [950.63]	283.36 (0.00) [0]
1425	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT	3/2018	/ (11/2019) [0/0]	828.29 (998.89) [828.29]	0.00 (0.00) [0]
1426	FOUR LANING OF YADGIRI - WARANGAL	12/2015	11/2018 (7/2019) [6/2020]	1,423.96 (897.03) [897.03]	796.56 (-526.93) [19]
1427	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365	3/2018	7/2019 (-) [0/0]	192.67 (-) [192.67]	107.37 (0.00) [0]
1428	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR	1/2017	10/2019 (-) [0/0]	605.08 (-) [605.08]	273.88 (0.00) [0]
1429	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN	2/2018	4/2020 (-) [4/2020]	426.52 (-) [426.52]	225.51 (0.00) [0]
1430	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT	1/2014	3/2016 (-) [0/0]	270.00 (-) [270.00]	19.84 (0.00) [0]
1431	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT	2/2018	11/2019 (-) [0/0]	294.13 (-) [294.13]	39.44 (0.00) [0]
1432	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS	2/2018	11/2019 (-) [0/0]	220.28 (-) [220.28]	37.58 (0.00) [0]
1433	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC	3/2018	9/2020 (-) [9/2020]	322.81 (-) [322.81]	1.66 (0.00) [0]
1434	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ	10/2016	3/2019 (-) [3/2020]	248.83 (-) [248.83]	91.52 (0.00) [12]
1435	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON	10/2016	2/2019 (-) [6/2020]	298.32 (-) [298.32]	83.57 (0.00) [16]
1436	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4	1/2018	12/2019 (-) [0/0]	230.03 (-) [230.03]	127.98 (0.00) [0]
1437	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59	2/2018	6/2020 (-) [6/2020]	206.13 (-) [206.13]	127.86 (0.00) [0]
1438	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR	1/2019	/ (-) [0/0]	193.19 (-) [193.19]	0.00 (0.00) [0]

1439	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH	1/2017	10/2019 (-) [0/0]	196.52 (-) [196.52]	103.22 (0.00) [0]
1440	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI	1/2017	12/2019 (-) [0/0]	283.00 (-) [283.00]	166.22 (0.00) [0]
1441	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037 OF THIRUMALAGIRI TO SURYAPET SE	1/2017	5/2019 (-) [0/0]	244.54 (-) [244.54]	138.52 (0.00) [0]
1442	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT	1/2017	5/2019 (-) [0/0]	359.27 (-) [359.27]	237.90 (0.00) [0]
1443	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION	1/2017	5/2019 (-) [3/2020]	300.00 (-) [300.00]	100.33 (0.00) [10]
	<u>Urban Development</u>				
1444	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD	10/2016	3/2020 (-) [5/2021]	209.84 (-) [209.84]	70.43 (0.00) [14]
	<u>TRIPURA</u>				
	<u>Civil Aviation</u>				
1445	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	9/2015	6/2019 (-) [0/0]	338.93 (-) [339.00]	213.50 (0.07) [0]
	<u>Railways</u>				
1446	AGARTALA-AKHAURA NL	4/2012	3/2020 (9/2021) [9/2021]	569.63 (670.00) [670.00]	82.81 (100.37) [18]
	<u>Road Transport And Highways</u>				
1447	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S	10/2014	3/2018 (12/2019) [0/0]	369.00 (-) [369.00]	319.05 (0.00) [0]
1448	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C	10/2016	8/2020 (-) [8/2020]	171.90 (-) [171.90]	23.19 (0.00) [0]
	<u>Urban Development</u>				
1449	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	3/2007	12/2015 (-) [0/0]	149.73 (173.00) [175.94]	176.65 (26.21) [0]
1450	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016 (-) [0/0]	202.61 (227.00) [227.00]	199.95 (24.39) [0]
1451	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	12/2016 (-) [0/0]	175.49 (206.71) [206.71]	141.28 (31.22) [0]
	<u>UTTAR PRADESH</u>				
	<u>Civil Aviation</u>				
1452	CCS INTERNATIONAL AIRPORT , LUCKNOW	6/2018	9/2021 (-) [9/2021]	1,383.00 (-) [1,383.00]	210.62 (0.00) [0]
	<u>Coal</u>				
1453	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	7/2016	11/2021 (-) [11/2021]	17,237.00 (-) [17,237.80]	8,596.47 (0.80) [0]
	<u>Health And Family Welfare</u>				
1454	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	7/2016	4/2020 (-) [10/2020]	785.00 (-) [715.06]	385.77 (-69.94) [6]
1455	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI	3/2018	/ (-) [4/2020]	268.84 (-) [268.84]	181.36 (0.00) [-]

	Petroleum				
1456	120 TMTPA LPG BOTTLING PLANT AT GORAKHPUR UP	3/2014	9/2019 (-) [0/0]	204.00 (-) [204.00]	148.58 (0.00) [0]
1457	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A	3/2018	12/2021 (-) [12/2021]	676.00 (-) [676.00]	271.05 (0.00) [0]
1458	BS-VI PROJECT AT MATHURA REFINERY	1/2018	9/2019 (-) [1/2020]	666.64 (-) [666.64]	493.90 (0.00) [4]
1459	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI	4/2017	4/2022 (-) [4/2022]	287.49 (-) [287.49]	138.25 (0.00) [0]
1460	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY	8/2017	8/2020 (-) [8/2020]	255.40 (-) [255.40]	6.53 (0.00) [0]
1461	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL	12/2017	12/2021 (-) [12/2021]	1,524.06 (-) [1,524.06]	22.01 (0.00) [0]
1462	REDEVELOPMENT/ EXPANSION OF MEERUT DEPOT FOR ENHANCING PRODUCT HANDLING CAPACITY	8/2016	11/2019 (-) [11/2019]	154.84 (-) [154.84]	128.71 (0.00) [0]
1463	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR	8/2017	8/2021 (-) [11/2021]	318.80 (-) [318.80]	63.90 (0.00) [3]
	Power				
1464	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP	12/2018	9/2020 (-) [9/2020]	587.44 (-) [587.44]	250.00 (0.00) [0]
1465	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP	3/2019	11/2020 (-) [11/2020]	349.00 (-) [349.00]	125.00 (0.00) [0]
1466	KHURJA SUPER THERMAL POWER PROJECT	3/2019	9/2023 (-) [9/2023]	11,089.42 (-) [11,089.42]	909.73 (0.00) [0]
1467	MUNPL-MEJA TPP - JV (2X660 MW)	4/2012	2/2017 (6/2020) [6/2020]	9,750.89 (-) [12,176.28]	10,103.00 (2,425.39) [40]
1468	TANDA TPP STAGE-II (2X660 MW)	9/2014	7/2019 (3/2020) [9/2020]	9,188.98 (-) [10,016.10]	7,036.74 (827.12) [14]
	Railways				
1469	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP	3/2013	/ (-) [0/0]	307.00 (-) [1,409.09]	0.00 (1,102.09) [0]
1470	AUNRIHAR - JAUNPUR PATCH DOUBLING .	4/2016	1/2022 (-) [1/2022]	600.00 (-) [600.00]	69.85 (0.00) [0]
1471	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI.	4/2016	1/2022 (-) [1/2022]	1,900.00 (-) [1,277.06]	0.00 (-622.94) [0]
1472	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	3/2012	12/2020 (-) [12/2022]	1,183.25 (-) [1,183.25]	1,184.32 (0.00) [24]
1473	BURHWAL - GONDA - 3RD RUNNING LINE.	4/2016	/ (-) [0/0]	602.50 (-) [714.34]	34.88 (111.84) [0]
1474	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	2/2008	3/2012 (-) [0/0]	171.10 (-) [275.08]	141.55 (103.98) [0]
1475	ETAH - KASGANJ - NEW LINE	4/2017	4/2017	276.90	0.00

			(-) [4/2022]	(-) [276.90]	(0.00) [60]
1476	ETAWAH-MAINPURI (NL),NCR	4/1997	12/2008 (-) [0/0]	120.00 (-) [346.00]	345.51 (226.00) [0]
1477	GHAZIPUR - AUNRIHAR (40 KM)	4/2014	/ (-) [0/0]	182.92 (-) [197.73]	0.00 (14.81) [0]
1478	INDARA - DOHRIGHAT GAUGE CONVERSION.	4/2016	4/2016 (-) [6/2020]	213.00 (-) [213.35]	9.63 (0.35) [50]
1479	JHANSI BINA DOUBLING	9/2016	3/2021 (-) [3/2021]	2,001.00 (-) [2,001.00]	416.59 (0.00) [0]
1480	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING	3/2018	3/2023 (-) [3/2023]	4,329.53 (-) [4,329.53]	3.90 (0.00) [0]
1481	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP	3/2013	/ (-) [0/0]	643.00 (-) [644.00]	0.00 (1.00) [0]
1482	KARAILA ROAD - SHAKTINAGAR DOUBLING	8/2015	3/2019 (-) [3/2021]	528.57 (-) [528.57]	128.55 (0.00) [24]
1483	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	4/2011	3/2019 (-) [3/2020]	927.01 (-) [1,200.00]	1,209.55 (272.99) [12]
1484	MATHURA-PLWAL 4TH LINE (80KM)	4/2015	3/2020 (-) [3/2020]	668.70 (668.00) [680.00]	330.00 (11.30) [0]
1485	MAU-GHAZIPUR-TARIGHAT NEW LINE	4/2015	3/2023 (-) [12/2024]	1,765.92 (-) [1,765.92]	674.40 (0.00) [21]
1486	NANPARA - NEPALGANJ GAUGE CONVERSION.	4/2017	4/2017 (-) [10/2022]	150.00 (-) [150.00]	0.00 (0.00) [66]
1487	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE	4/2017	1/2018 (-) [0/0]	1,343.00 (-) [1,476.15]	0.00 (133.15) [0]
1488	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION	4/2017	4/2017 (-) [1/2020]	622.50 (427.00) [426.74]	240.48 (-195.76) [33]
1489	RAMNA - SINGRAULI DOUBLING	8/2015	3/2020 (-) [3/2021]	2,436.21 (-) [2,436.21]	681.43 (0.00) [12]
1490	ROSA-SITAPUR CANTT-BURHWAL DOUBLING	3/2015	3/2022 (-) [12/2019]	1,295.42 (-) [1,295.42]	473.91 (0.00) [0]
1491	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING.	4/2016	12/2019 (-) [4/2021]	1,177.96 (-) [1,028.95]	26.06 (-149.01) [16]
1492	UNCHAHAAR-AMETHI	4/2012	/ (-) [3/2023]	1,229.00 (-) [1,230.00]	103.72 (1.00) [-]
1493	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	4/2015	3/2022 (-) [12/2024]	943.60 (-) [750.56]	485.98 (-193.04) [33]
<u>Road Transport And Highways</u>					
1494	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125	9/2015	9/2016 (3/2018) [3/2018]	368.73 (-) [368.73]	239.04 (0.00) [0]
1495	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-	11/2010	3/2017	305.49	131.08

	52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE		(-) [0/0]	(-) [305.49]	(0.00) [0]
1496	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232	4/2014	1/2016 (-) [0/0]	351.34 (-) [351.34]	433.68 (0.00) [0]
1497	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI	4/2014	1/2016 (-) [0/0]	495.78 (-) [495.78]	633.24 (0.00) [0]
1498	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	7/2012	1/2014 (-) [0/0]	291.36 (-) [291.36]	459.07 (0.00) [0]
1499	2-LANING WITH PS SITARGANJ BAREILY SECTION	6/2014	1/2016 (-) [0/0]	301.04 (-) [301.04]	207.94 (0.00) [0]
1500	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500	8/2016	4/2019 (-) [11/2019]	2,016.00 (-) [2,016.00]	1,996.00 (0.00) [0]
1501	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C	3/2018	/ (-) [0/0]	1,120.57 (1,332.00) [1,332.00]	510.96 (211.43) [0]
1502	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (	3/2016	/ (-) [1/2020]	1,668.00 (-) [1,668.00]	946.08 (0.00) [-]
1503	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I)	12/2015	6/2016 (-) [0/0]	611.65 (-) [611.65]	728.24 (0.00) [0]
1504	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00	3/2016	/ (-) [7/2020]	1,408.00 (-) [1,408.00]	442.70 (0.00) [-]
1505	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00	3/2016	/ (-) [4/2020]	1,737.00 (-) [1,737.00]	1,159.07 (0.00) [-]
1506	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR)	3/2016	/ (3/2017) [0/0]	1,404.50 (3,267.94) [1,404.50]	2,977.58 (0.00) [0]
1507	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	3/2016	4/2019 (-) [0/0]	1,587.49 (-) [2,982.00]	276.87 (1,394.51) [0]
1508	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPU	3/2016	/ (-) [0/0]	1,396.74 (-) [1,396.74]	227.26 (0.00) [0]
1509	6 LANING OF AGRA - ETAWAH BYPASS	7/2015	1/2019 (-) [0/0]	1,657.20 (-) [1,657.20]	2,345.00 (0.00) [0]
1510	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	3/2017	3/2020 (6/2020) [6/2020]	2,064.99 (-) [2,447.00]	2,029.34 (382.01) [3]
1511	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT- MUZAFFARN	12/2017	/ (3/2020) [12/2020]	207.00 (-) [207.00]	34.77 (0.00) [-]
1512	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020	3/2016	4/2019 (-) [0/0]	676.73 (-) [676.73]	945.17 (0.00) [0]
1513	BAREILY-SITAPUR (NH-24)	3/2011	9/2013 (-) [0/0]	1,046.00 (-) [1,046.00]	805.19 (0.00) [0]
1514	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA	2/2018	/ (2/2019) [0/0]	972.77 (1,444.25) [972.77]	494.71 (0.00) [0]
1515	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700	12/2016	/ (-)	534.55 (-)	433.62 (-3.55)

	OF NH-28 T		[9/2019]	[531.00]	[0]
1516	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O	12/2017	/	305.00	0.00
			(-)	(-)	(0.00)
			[0/0]	[305.00]	[0]
1517	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO	3/2018	/	1,117.84	0.00
			(-)	(-)	(0.00)
			[12/2021]	[1,117.84]	[-]
1518	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650	1/2017	/	450.68	397.62
			(-)	(-)	(0.00)
			[0/0]	[450.68]	[0]
1519	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B	1/2014	3/2016	282.41	155.53
			(-)	(-)	(0.00)
			[0/0]	[282.41]	[0]
1520	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM	1/2016	6/2019	1,081.57	1,041.85
			(12/2016)	(-)	(-23.97)
			[9/2019]	[1,057.60]	[0]
1521	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM	12/2017	/	1,232.21	562.94
			(2/2018)	(3,207.63)	(-145.21)
			[5/2020]	[1,087.00]	[-]
1522	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO	3/2017	3/2020	1,989.00	892.35
			(11/2017)	(2,602.09)	(0.00)
			[5/2020]	[1,989.00]	[2]
1523	ETAWAH CHAKERI	3/2013	9/2015	1,573.00	2,078.25
			(-)	(-)	(0.00)
			[0/0]	[1,573.00]	[0]
1524	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP	2/2018	/	670.50	44.24
			(-)	(-)	(0.00)
			[0/0]	[670.50]	[0]
1525	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS	3/2018	/	809.07	176.96
			(-)	(1,065.70)	(0.00)
			[0/0]	[809.07]	[0]
1526	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR.	3/2018	/	925.40	563.83
			(-)	(1,197.00)	(271.60)
			[0/0]	[1,197.00]	[0]
1527	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II)	12/2015	6/2018	667.00	549.07
			(-)	(3,007.86)	(0.00)
			[4/2020]	[667.00]	[22]
1528	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III)	6/2016	7/2018	667.00	464.05
			(-)	(2,257.49)	(0.00)
			[4/2020]	[667.00]	[21]
1529	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I)	1/2016	6/2018	1,027.53	601.13
			(-)	(2,433.38)	(0.00)
			[6/2020]	[1,027.53]	[24]
1530	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II)	1/2016	6/2018	815.28	520.89
			(-)	(2,182.03)	(0.00)
			[6/2020]	[815.28]	[24]
1531	FOUR LANING OF VARANASI BYPASS	5/2015	5/2017	261.09	240.96
			(-)	(275.00)	(0.00)
			[0/0]	[261.09]	[0]
1532	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONALI - GORAKHPUR ROAD (J	3/2018	8/2020	288.30	41.74
			(-)	(-)	(0.00)
			[8/2020]	[288.30]	[0]
1533	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2	3/2017	3/2020	1,373.28	571.96
			(-)	(-)	(0.00)
			[11/2020]	[1,373.28]	[8]
1534	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	3/2017	3/2020	1,184.71	563.15
			(-)	(-)	(125.29)
			[8/2020]	[1,310.00]	[5]
1535	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791	3/2016	4/2019	899.00	641.51
			(7/2020)	(-)	(0.00)
			[7/2020]	[899.00]	[15]

1536	GHAZIABAD-ALIGARH NH-91	2/2011	8/2013 (-) [0/0]	1,141.00 (-) [1,141.00]	1,715.42 (0.00) [0]
1537	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T	11/2018	/ (-) [0/0]	281.45 (-) [281.45]	0.00 (0.00) [0]
1538	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 KM	11/2018	12/2020 (-) [12/2020]	281.45 (-) [281.45]	2.36 (0.00) [0]
1539	MEERUT-BULANDSHAHR	1/2016	/ (10/2019) [2/2020]	683.24 (868.77) [987.94]	727.69 (304.70) [-]
1540	R AND U FROM KM 385.00 TO KM 420.000 TO 2- LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404	12/2016	10/2019 (4/2020) [4/2020]	209.10 (-) [209.10]	160.28 (0.00) [6]
1541	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS	11/2016	/ (-) [0/0]	326.99 (327.00) [326.99]	4.03 (0.00) [0]
1542	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS	3/2016	9/2020 (-) [9/2020]	296.50 (-) [296.50]	74.77 (0.00) [0]
1543	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU	3/2018	/ (-) [0/0]	1,025.80 (-) [677.07]	203.25 (-348.73) [0]
1544	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA	3/2018	/ (-) [0/0]	1,115.28 (-) [770.04]	288.52 (-345.24) [0]
1545	REHABILITATION AND UPGRADATION OF ALLAHABAD - MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2-	10/2016	2/2019 (-) [7/2019]	239.63 (-) [239.63]	212.53 (0.00) [0]
1546	REHABILITATION AND UPGRADATION OF BARAICH - SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA	3/2016	12/2019 (-) [12/2019]	388.83 (-) [388.83]	304.70 (0.00) [0]
1547	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750	3/2018	4/2020 (-) [4/2020]	263.89 (242.05) [242.05]	139.94 (-21.84) [0]
1548	REHABILITATION AND UPGRADATION OF HARPALPUR - SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2- LANE	3/2016	11/2019 (-) [3/2020]	208.50 (-) [208.50]	141.54 (0.00) [4]
1549	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH	10/2013	3/2017 (-) [10/2019]	445.89 (653.00) [653.29]	469.64 (207.40) [0]
1550	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F	3/2016	1/2020 (-) [1/2020]	599.34 (-) [599.34]	492.15 (0.00) [0]
1551	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF	3/2018	2/2020 (-) [2/2020]	185.18 (-) [185.18]	79.93 (0.00) [0]
1552	REHABILITATION AND UPGRADATION OF TULSIPUR - BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730	3/2016	5/2019 (-) [3/2020]	249.50 (-) [249.50]	160.60 (0.00) [10]
1553	REHABILITATION AND UPGRADATION OF ALLAHABAD - MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT	10/2016	3/2020 (-) [3/2020]	218.90 (-) [218.90]	64.59 (0.00) [0]
1554	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230	3/2018	/ (-) [0/0]	306.59 (-) [306.59]	0.00 (0.00) [0]
1555	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P	11/2016	9/2019 (-) [10/2019]	215.16 (215.00) [215.16]	160.61 (0.00) [0]
1556	REHABILITATION AND UPGRADATION OF KALUPUR-	3/2016	1/2020	240.30	198.06

	LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH		(-) [3/2020]	(240.00) [240.30]	(0.00) [2]
1557	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA	10/2016	3/2020 (-) [3/2020]	218.94 (219.00) [218.94]	120.69 (0.00) [0]
1558	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO	10/2016	10/2018 (-) [9/2019]	176.94 (177.00) [176.94]	141.11 (0.00) [0]
1559	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO	7/2016	10/2019 (-) [6/2020]	208.88 (-) [208.88]	95.59 (0.00) [8]
1560	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270	10/2013	3/2017 (-) [0/0]	445.89 (-) [653.29]	464.05 (207.40) [0]
1561	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH – 14	11/2017	1/2019 (-) [0/0]	2,159.00 (-) [2,159.00]	867.86 (0.00) [0]
1562	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA	3/2018	/ (-) [0/0]	2,140.93 (-) [2,140.93]	1,230.96 (0.00) [0]
1563	VARANASI RING ROAD PKG - I	1/2018	/ (-) [0/0]	450.77 (929.89) [450.77]	0.00 (0.00) [0]
1564	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH	5/2013	8/2015 (-) [3/2020]	164.54 (165.00) [164.54]	127.34 (0.00) [55]
1565	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE	5/2013	8/2015 (-) [12/2019]	164.54 (-) [164.54]	126.41 (0.00) [0]
	<u>Steel</u>				
1566	FORGED WHEEL PLANT	4/2014	9/2018 (2/2020) [2/2020]	1,682.85 (-) [1,682.85]	1,341.85 (0.00) [17]
	<u>Urban Development</u>				
1567	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR	11/2017	3/2020 (11/2020) [3/2020]	171.72 (-) [171.72]	45.00 (0.00) [0]
1568	LUCKNOW METRO RAIL CORPORATION LTD	1/2016	3/2019 (-) [0/0]	6,928.00 (6,928.00) [6,928.00]	2,536.77 (0.00) [0]
	<u>Water Resources</u>				
1569	FARRUKHABAD I AND D AND STP WORKS HAM	10/2017	3/2022 (-) [3/2022]	213.62 (-) [213.62]	0.00 (0.00) [0]
1570	INTEGRATED PROJECT FOR DEVELOPMENT OF STPS IN ALLAHABAD ALONG WITH EXISTING ASSETS	3/2018	9/2021 (-) [9/2021]	904.00 (-) [904.00]	0.00 (0.00) [0]
1571	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH	1/2019	10/2021 (-) [10/2021]	206.05 (-) [206.05]	1.57 (0.00) [0]
1572	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH	1/2019	12/2021 (-) [12/2021]	231.79 (-) [231.79]	0.00 (0.00) [0]
1573	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH	3/2019	8/2021 (-) [8/2021]	271.39 (-) [271.39]	0.00 (0.00) [0]
1574	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH	3/2019	7/2021 (-) [7/2021]	298.12 (-) [298.12]	0.00 (0.00) [0]
1575	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND	5/2017	9/2021 (-)	767.59 (-)	0.01 (0.00)

	JHUSI AREA		[9/2021]	[767.59]	[0]
1576	MATHURA SEWERAGE SCHEME	12/2017	12/2020 (-) [12/2020]	460.45 (-) [460.45]	56.83 (0.00) [0]
1577	REHABILITATION RENOVATION OF AGRA SEWERAGE SCHEME INTERCEPTION AND DIVERSION WORKS IN AGRA UTTAR PR	12/2018	8/2021 (-) [8/2021]	857.26 (-) [857.26]	0.00 (0.00) [0]
1578	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA	2/2017	11/2019 (2/2020) [2/2020]	161.31 (-) [161.31]	37.60 (0.00) [3]
1579	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH	2/2019	6/2022 (-) [6/2022]	681.78 (-) [681.78]	0.00 (0.00) [0]
1580	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WORKS AT AGRA	2/2019	8/2021 (-) [8/2021]	317.19 (-) [317.19]	0.00 (0.00) [0]
1581	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA	2/2011	12/2019 (3/2020) [3/2020]	279.91 (-) [279.91]	199.59 (0.00) [3]
1582	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR	10/2016	8/2020 (-) [8/2020]	370.40 (430.49) [370.40]	268.59 (0.00) [0]
1583	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS	3/2018	9/2021 (-) [9/2021]	967.23 (-) [967.23]	0.00 (0.00) [0]
	<u>UTTARAKHAND</u>				
	<u>Civil Aviation</u>				
1584	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN	7/2018	9/2020 (-) [9/2020]	353.27 (-) [353.27]	114.29 (0.00) [0]
	<u>Petroleum</u>				
1585	SITARGANJ LPG PROJECT	2/2017	2/2020 (-) [10/2020]	160.10 (-) [160.10]	54.94 (0.00) [8]
	<u>Power</u>				
1586	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	7/2012	8/2017 (-) [0/0]	1,527.00 (-) [1,801.07]	148.93 (274.07) [0]
1587	NAITWAR MORI HEP	10/2017	12/2021 (-) [12/2021]	648.33 (-) [648.33]	310.91 (0.00) [0]
1588	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	3/2013 (12/2020) [12/2021]	2,978.48 (5,867.38) [5,867.38]	4,346.71 (2,888.90) [105]
1589	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	8/2008	6/2013 (-) [12/2022]	2,491.58 (-) [4,397.80]	1,858.35 (1,906.22) [114]
	<u>Railways</u>				
1590	HARIDWAR-LAKSAR	4/2012	/ (-) [6/2020]	219.83 (-) [346.63]	233.23 (126.80) [-]
1591	KICHHA-KHATIMA (NL) - NER	4/2003	/ (-) [0/0]	142.45 (-) [228.40]	0.15 (85.95) [0]
1592	RISHIKESH - KARNAPRAYAG NEW LINE	4/2011	12/2024 (-) [3/2025]	16,216.00 (-) [16,216.00]	1,941.37 (0.00) [3]
	<u>Road Transport And Highways</u>				
1593	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI	3/2018	6/2018 (-) [0/0]	403.36 (-) [403.36]	99.65 (0.00) [0]

1594	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA	3/2018	5/2018 (-) [0/0]	417.24 (-) [417.24]	112.62 (0.00) [0]
1595	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	11/2012	7/2018 (12/2019) [2/2020]	605.84 (-) [722.46]	722.46 (116.62) [19]
1596	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900	3/2016	/ (-) [2/2020]	1,443.00 (-) [1,443.00]	1,246.85 (0.00) [-]
1597	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399	3/2018	5/2018 (-) [0/0]	274.31 (-) [274.31]	29.13 (0.00) [0]
1598	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK)	3/2018	7/2018 (-) [0/0]	1,383.78 (-) [1,383.78]	138.75 (0.00) [0]
1599	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN	5/2018	5/2020 (-) [5/2020]	248.00 (-) [248.00]	0.00 (0.00) [0]
1600	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88	3/2016	/ (10/2020) [10/2020]	720.00 (-) [720.00]	343.72 (0.00) [-]
1601	HARIDWAR DEHRADUN APPROVED LENGTH 69	11/2011	10/2013 (-) [8/2020]	478.51 (-) [478.00]	315.11 (-0.51) [82]
1602	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG	11/2017	11/2019 (-) [0/0]	232.81 (-) [232.81]	59.44 (0.00) [0]
1603	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION	11/2017	11/2019 (-) [0/0]	283.51 (-) [283.51]	126.38 (0.00) [0]
1604	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	12/2017	12/2019 (-) [0/0]	257.34 (-) [257.34]	62.79 (0.00) [0]
1605	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	12/2017	12/2019 (-) [0/0]	200.34 (-) [200.34]	31.00 (0.00) [0]
1606	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	6/2017	6/2019 (-) [0/0]	282.08 (-) [282.08]	77.05 (0.00) [0]
1607	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR	2/2018	2/2020 (-) [2/2020]	418.88 (-) [418.88]	88.00 (0.00) [0]
1608	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	11/2017	11/2019 (-) [0/0]	266.52 (-) [266.52]	144.27 (0.00) [0]
1609	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER	8/2016	12/2017 (-) [0/0]	234.88 (-) [208.89]	118.26 (-25.99) [0]
1610	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K	2/2018	/ (-) [0/0]	293.68 (-) [293.68]	11.57 (0.00) [0]
1611	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00	3/2018	/ (-) [0/0]	460.73 (-) [461.00]	0.00 (0.27) [0]
1612	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00	12/2017	12/2019 (-) [0/0]	248.22 (-) [248.22]	57.20 (0.00) [0]
<u>Urban Development</u>					
1613	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	12/2013 (-) [0/0]	114.26 (266.00) [266.00]	0.00 (151.74) [0]

	<u>Water Resources</u>				
1614	INTERCEPTION AND DIVERSION (I&D) WITH STP AT RISHIKESH	3/2017	11/2019 (-) [0/0]	158.00 (-) [158.00]	0.00 (0.00) [0]
1615	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI	3/2017	8/2019 (2/2020) [2/2020]	273.37 (-) [273.37]	53.19 (0.00) [6]
	<u>WEST BENGAL</u>				
	<u>Civil Aviation</u>				
1616	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA	1/2019	11/2021 (-) [11/2021]	264.99 (-) [264.99]	0.42 (0.00) [0]
1617	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	1/2016	3/2020 (-) [12/2020]	219.91 (-) [219.91]	65.45 (0.00) [9]
	<u>Coal</u>				
1618	JHANJRA COMBINED PR(3.50 MTY)	11/2015	3/2022 (-) [3/2022]	602.86 (-) [602.86]	318.97 (0.00) [0]
1619	NAKRAKONDA KUMARDIH B OCP	8/2018	3/2029 (-) [3/2029]	502.68 (-) [502.68]	0.00 (0.00) [0]
1620	PARASEA- BELBAID REORGANISATION UG MINE	7/2019	3/2027 (-) [3/2027]	826.42 (-) [826.42]	0.00 (0.00) [0]
1621	RANIGANJ MASTER PLAN	8/2009	8/2019 (-) [8/2024]	2,661.73 (-) [5,146.48]	364.72 (2,484.75) [60]
1622	SIDULI MINE (OC AND UG)	5/2018	3/2026 (-) [3/2026]	535.18 (-) [535.18]	0.19 (0.00) [0]
1623	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	8/2012	3/2018 (-) [10/2020]	1,055.05 (-) [1,055.05]	562.60 (0.00) [31]
1624	TILABONI UG MINE	2/2019	3/2027 (-) [3/2027]	916.62 (-) [916.62]	0.00 (0.00) [0]
	<u>Health And Family Welfare</u>				
1625	CNCI KOLKATA WEST BENGAL	8/2016	9/2018 (-) [5/2019]	244.00 (-) [248.00]	224.92 (4.00) [0]
1626	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	5/2017 (-) [7/2019]	168.90 (-) [191.20]	169.51 (22.30) [0]
1627	HOSPITAL AND TEACHING- AIIMS KALYANI	4/2018	/ (-) [7/2020]	651.99 (-) [651.99]	285.33 (0.00) [-]
1628	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	8/2017	3/2019 (-) [7/2020]	355.15 (-) [355.15]	233.51 (0.00) [16]
	<u>Petroleum</u>				
1629	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL	3/2018	9/2022 (-) [6/2021]	3,712.00 (-) [3,696.00]	1,001.53 (-16.00) [-15]
1630	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY	5/2018	9/2019 (-) [2/2020]	2,934.40 (-) [2,934.40]	1,928.10 (0.00) [5]
1631	DURGAPUR-HALDIA PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	1,740.00 (-) [1,740.00]	612.62 (0.00) [0]
1632	HALDIA BARAUNI PRODUCT PIPELINE	4/2016	12/2020	1,021.00	4.45

			(-) [12/2020]	(-) [1,021.00]	(0.00) [0]
1633	HALDIA LPG IMPORT FACILITY	3/2015	10/2018 (2/2020) [2/2020]	694.00 (1,097.54) [1,097.54]	856.34 (403.54) [16]
1634	KHARAGPUR LPG BOTTLING PLANT	4/2017	4/2020 (-) [3/2021]	163.02 (-) [163.02]	59.14 (0.00) [11]
	<u>Power</u>				
1635	DURGAPUR PP-III (2X20 MW) - NSPCL	12/2016	11/2018 (-) [8/2020]	529.68 (-) [529.68]	294.18 (0.00) [21]
1636	EASTERN REGION STRENGTHENING SCHEME-XV	4/2016	4/2018 (1/2020) [1/2020]	454.11 (-) [454.11]	297.68 (0.00) [21]
1637	RAMMAM-III HEPP (3X40 MW)	9/2014	9/2019 (2/2022) [11/2022]	1,381.84 (-) [1,592.34]	526.08 (210.50) [38]
	<u>Railways</u>				
1638	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	4/1998	3/2003 (3/2030) [3/2030]	1,027.40 (1,966.70) [2,373.00]	485.04 (1,345.60) [324]
1639	BARDHAMAN-KATWA (GC)	4/2007	12/2010 (12/2017) [3/2025]	1,106.62 (-) [1,091.59]	877.32 (-15.03) [171]
1640	BAZAR SAU -AZIMGANJ JN. DOUBLING	4/2012	/ (-) [9/2021]	255.64 (-) [272.20]	196.05 (16.56) [-]
1641	BOWAICHANDI-ARAMBAGH	4/2010	/ (3/2025) [3/2025]	267.37 (-) [620.00]	40.99 (352.63) [-]
1642	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR	4/2009	/ (-) [3/2025]	573.78 (-) [268.52]	0.03 (-305.26) [-]
1643	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	3/2013	3/2016 (-) [6/2021]	4,874.58 (-) [8,574.97]	5,892.72 (3,700.39) [63]
1644	HOWRAH-AMTA-CHAMPADANGA NL (SER)	4/1974	3/2007 (3/2007) [0/0]	393.46 (154.30) [1,026.00]	182.49 (632.54) [0]
1645	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	4/2010	/ (3/2022) [3/2022]	221.42 (-) [380.00]	38.18 (158.58) [-]
1646	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	4/1983	3/2019 (-) [3/2020]	297.32 (-) [614.00]	275.07 (316.68) [12]
1647	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN	2/1999	4/2010 (-) [0/0]	380.60 (-) [1,871.00]	1,087.60 (1,490.40) [0]
1648	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM)	4/2016	12/2021 (-) [3/2020]	602.27 (-) [612.00]	344.08 (9.73) [-21]
1649	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	4/2010	3/2014 (-) [12/2025]	2,298.42 (-) [2,733.86]	40.13 (435.44) [141]
1650	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	4/2010	3/2016 (-) [3/2025]	2,913.51 (-) [4,639.00]	871.04 (1,725.49) [108]
1651	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP)	4/2010	3/2016 (-) [0/0]	2,397.72 (-) [2,397.72]	197.20 (0.00) [0]

1652	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	4/2010	3/2016 (-) [3/2025]	3,951.98 (-) [4,724.30]	2,307.00 (772.32) [108]
1653	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	4/2000	3/2019 (12/2009) [3/2025]	1,188.91 (-) [1,619.48]	872.43 (430.57) [72]
1654	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	3/2000	12/2006 (-) [0/0]	1,049.69 (-) [3,404.92]	3,837.57 (2,355.23) [0]
Road Transport And Highways					
1655	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	12/2015	6/2018 (-) [0/0]	1,083.00 (-) [1,083.00]	1,487.87 (0.00) [0]
1656	4-LANING OF BRAHAMPURE-FARAKA	2/2011	8/2013 (-) [3/2021]	998.79 (-) [998.79]	1,822.59 (0.00) [91]
1657	4-LANING OF FARAKA-RAIGANJ	2/2011	8/2013 (-) [5/2020]	1,078.84 (-) [1,078.84]	2,195.64 (0.00) [81]
1658	6-LANING OF DHANKUNI-KHARAGPUR SECTION	4/2012	9/2014 (-) [3/2020]	1,396.18 (-) [1,396.18]	2,894.94 (0.00) [66]
1659	CONSTRUCTION OF ISLAMPUR BY PASS	10/2015	/ (-) [1/2020]	361.15 (-) [361.15]	186.64 (0.00) [-]
1660	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITTA AND PANITNAKI I	3/2017	6/2018 (-) [0/0]	158.65 (-) [158.65]	59.53 (0.00) [0]
1661	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H	3/2016	11/2018 (11/2019) [11/2019]	271.17 (291.20) [291.20]	110.98 (20.03) [0]
1662	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND	3/2016	8/2019 (-) [8/2021]	160.27 (213.97) [213.97]	20.11 (53.70) [24]
1663	CONSTRUCTION OF ROB –FLYOVER AT RANICHAK, HALDIA	3/2016	11/2018 (8/2020) [8/2020]	229.37 (-) [229.37]	112.94 (0.00) [21]
1664	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N	6/2016	8/2019 (-) [8/2021]	236.78 (263.26) [263.26]	59.92 (26.48) [24]
1665	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO	3/2018	10/2020 (-) [10/2020]	254.30 (254.30) [254.30]	53.46 (0.00) [0]
1666	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA	9/2016	8/2018 (-) [9/2019]	767.03 (767.03) [767.03]	601.10 (0.00) [0]
1667	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O	8/2014	11/2017 (5/2019) [5/2019]	600.87 (720.97) [720.97]	659.24 (120.10) [0]
1668	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O	8/2014	11/2017 (6/2019) [6/2019]	823.20 (937.76) [937.76]	751.29 (114.56) [0]
1669	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA)	3/2018	/ (-) [7/2021]	1,261.98 (-) [1,261.98]	793.49 (0.00) [-]
1670	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7	4/2014	8/2017 (7/2019) [7/2019]	279.70 (398.52) [398.52]	322.91 (118.82) [0]
1671	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAL-CHAN	1/2017	9/2019 (-) [0/0]	396.86 (396.86) [396.86]	185.31 (0.00) [0]

1672	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL	1/1991	3/2018 (-) [0/0]	322.00 (-) [322.00]	56.41 (0.00) [0]
1673	SIX-LANING OF BARWA ADDA-PANAGARH	4/2014	/ (-) [0/0]	1,665.00 (-) [1,665.00]	4,357.89 (0.00) [0]
1674	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10	3/2017	11/2019 (-) [0/0]	202.69 (202.69) [202.69]	103.14 (0.00) [0]
1675	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4	2/2018	11/2020 (-) [0/0]	218.70 (218.70) [218.70]	45.72 (0.00) [0]
1676	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19.	2/2018	9/2020 (-) [0/0]	426.18 (426.18) [426.18]	224.22 (0.00) [0]
	<u>Steel</u>				
1677	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E	12/2018	9/2020 (-) [9/2020]	263.36 (-) [263.36]	29.03 (0.00) [0]
	<u>Urban Development</u>				
1678	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	2/2014	8/2016 (-) [1/2020]	156.57 (-) [156.57]	159.35 (0.00) [41]
1679	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG	8/2012	3/2016 (-) [0/0]	185.37 (-) [185.37]	178.30 (0.00) [0]
1680	NSG AT KOLKATA	10/2014	4/2018 (6/2020) [6/2020]	162.88 (179.10) [162.88]	148.52 (0.00) [26]
	<u>Water Resources</u>				
1681	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR	2/2014	12/2019 (2/2020) [2/2020]	274.76 (-) [274.76]	171.80 (0.00) [2]
1682	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS	1/2019	4/2022 (-) [4/2022]	384.96 (-) [384.96]	0.00 (0.00) [0]
1683	I AND D AND STP WORKS AT BURDWAN WEST BENGAL	12/2018	4/2022 (-) [4/2022]	234.31 (-) [234.31]	0.00 (0.00) [0]
1684	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS	3/2018	6/2022 (-) [6/2022]	165.16 (-) [165.16]	0.00 (0.00) [0]
1685	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH	5/2018	2/2022 (-) [2/2022]	160.00 (-) [160.00]	0.00 (0.00) [0]
1686	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPURL	3/2019	4/2022 (-) [4/2022]	287.53 (-) [287.53]	0.00 (0.00) [0]
1687	INTERCEPTION AND DIVERSION WITH STP AT BALLY	10/2017	12/2021 (-) [12/2021]	164.93 (-) [164.93]	0.00 (0.00) [0]
1688	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA	5/2018	2/2022 (-) [2/2022]	198.43 (-) [198.43]	0.00 (0.00) [0]
1689	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA	8/2017	9/2022 (-) [9/2022]	307.12 (-) [307.12]	0.00 (0.00) [0]
1690	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI	1/2018	12/2021 (-) [12/2021]	172.10 (-) [172.10]	0.00 (0.00) [0]
1691	INTERCEPTION, DIVERSION AND TREATMENT WORKS	8/2017	12/2021	185.22	0.00

	AT HOWRAH		(-) [12/2021]	(-) [185.22]	(0.00) [0]
1692	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE	12/2014	4/2020 (-) [4/2020]	272.32 (-) [272.32]	191.36 (0.00) [0]
	Total			20,75,212.70 (7,26,596.82) [24,78,016.45]	10,97,604.64 (4,02,803.75)

North- East Central Sector Ongoing Projects List

Annexure-XX

Details of Central Sector Projects Costing Rs.150 crore and above (as on 31.01.2020)					
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	ARUNACHAL PRADESH				
	Power				
1	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009 (6/2020) [6/2020]	2,496.90 (7,927.34) [7,927.34]	7,743.76 (5,430.44) [126]
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (8/2023) [8/2023]	6,285.33 (-) [19,496.34]	11,842.12 (13,211.01) [155]
	Road Transport And Highways				
3	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN	3/2015	/ (-) [0/0]	172.75 (-) [172.75]	120.18 (0.00) [0]
4	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	3/2015	6/2018 (-) [3/2020]	394.00 (-) [394.00]	325.08 (0.00) [21]
5	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59	3/2015	5/2018 (-) [8/2019]	194.11 (-) [194.11]	181.03 (0.00) [0]
6	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS	10/2015	1/2019 (-) [0/0]	179.82 (-) [179.82]	197.77 (0.00) [0]
7	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX	10/2015	/ (1/2016) [1/2019]	210.50 (210.50) [210.50]	122.09 (0.00) [0]
8	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROM KM.583.450	1/2016	11/2016 (-) [0/0]	183.65 (-) [183.65]	129.11 (0.00) [0]
9	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST	11/2016	/ (-) [9/2020]	243.89 (-) [243.89]	128.46 (0.00) [-]
10	BORDUMSA NAMCHIK (BURIDEHING - JAIRAMPUR) ROAD ON NH-52B (NEW NH-215) FROM KM. 0.15 (STARTING CHAIN	7/2015	/ (-) [0/0]	189.91 (-) [189.91]	154.43 (0.00) [0]
11	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 37.500 TO KM	5/2016	/ (-) [0/0]	259.52 (-) [259.52]	184.51 (0.00) [0]
12	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120.	12/2016	/ (-) [0/0]	200.44 (-) [200.44]	79.80 (0.00) [0]
13	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50	9/2016	/ (-) [0/0]	568.92 (-) [568.92]	172.88 (0.00) [0]
14	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5	12/2016	/ (-) [0/0]	188.78 (-) [188.78]	59.98 (0.00) [0]
15	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	12/2016	1/2017 (-) [1/2020]	138.93 (155.00) [155.00]	79.91 (16.07) [36]

16	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37	4/2016	/ (-) [9/2020]	245.79 (-) [245.79]	129.43 (0.00) [-]
17	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM.	4/2016	10/2016 (-) [10/2019]	198.00 (-) [198.00]	184.62 (0.00) [0]
18	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH	7/2015	10/2018 (9/2015) [9/2018]	197.16 (197.16) [197.16]	81.53 (0.00) [0]
19	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF	3/2017	/ (-) [0/0]	1,718.59 (-) [1,718.59]	204.77 (0.00) [0]
20	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	1/2017	3/2017 (-) [3/2022]	1,253.10 (-) [1,253.10]	204.77 (0.00) [60]
21	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	2/2017	4/2017 (2/2018) [2/2021]	167.28 (167.28) [167.28]	21.54 (0.00) [46]
22	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS	2/2017	4/2017 (2/2018) [2/2021]	216.71 (216.71) [216.71]	25.17 (0.00) [46]
23	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K	3/2018	/ (-) [0/0]	392.60 (-) [392.60]	0.00 (0.00) [0]
24	FUNDED)CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH	11/2015	/ (-) [12/2020]	434.06 (-) [434.06]	172.89 (0.00) [-]
25	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017 (3/2018) [3/2021]	284.09 (284.09) [284.09]	96.13 (0.00) [47]
26	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017 (-) [0/0]	195.23 (-) [195.23]	62.01 (0.00) [0]
27	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	2/2017	4/2017 (-) [0/0]	203.36 (-) [203.36]	72.88 (0.00) [0]
28	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	194.66 (-) [194.66]	84.11 (0.00) [0]
29	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	198.22 (-) [198.22]	84.11 (0.00) [0]
30	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	3/2012	5/2012 (5/2015) [12/2019]	207.03 (389.45) [389.45]	308.09 (182.42) [0]
31	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	2/2017	4/2017 (2/2018) [2/2021]	180.57 (180.57) [180.57]	16.80 (0.00) [46]
32	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS	2/2017	4/2017 (2/2018) [2/2021]	168.32 (168.32) [168.32]	40.78 (0.00) [46]
33	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	12/2011	2/2012 (-) [0/0]	156.63 (276.00) [276.00]	147.65 (119.37) [0]
34	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P	11/2010	3/2011 (-) [0/0]	305.49 (-) [305.49]	131.08 (0.00) [0]
35	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI	1/2017	/ (-) [0/0]	256.66 (-) [256.66]	24.14 (0.00) [0]
36	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713)	2/2017	/	175.06	29.08

	FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0		(4/2019) [4/2022]	(175.06) [175.06]	(0.00) [-]
37	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1	2/2017	/ (4/2019) [4/2022]	176.12 (176.12) [176.12]	28.16 (0.00) [-]
38	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D	2/2017	/ (2/2018) [2/2021]	199.02 (199.02) [199.02]	13.82 (0.00) [-]
39	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D	2/2017	/ (2/2018) [2/2021]	184.88 (184.88) [184.88]	7.68 (0.00) [-]
40	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU	9/2011	/ (3/2020) [0/0]	1,979.00 (-) [1,979.00]	1,189.58 (0.00) [0]
	ASSAM				
	Civil Aviation				
41	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	3/2021 (-) [3/2021]	859.86 (-) [860.00]	232.44 (0.14) [0]
	Health And Family Welfare				
42	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021 (8/2021) [10/2021]	875.00 (-) [747.80]	137.27 (-127.20) [5]
	Petroleum				
43	BS VI PROJECT AT GUWAHATI REFINERY	8/2018	2/2020 (-) [4/2020]	557.00 (-) [557.00]	313.62 (0.00) [2]
44	BS-VI PROJECT AT BONGAIGAON REFINERY	5/2018	9/2019 (-) [2/2020]	1,222.00 (-) [1,222.00]	739.04 (0.00) [5]
45	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN	6/2016	8/2020 (-) [8/2020]	224.75 (-) [224.75]	98.98 (0.00) [0]
46	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	7/2011	1/2019 (-) [0/0]	350.00 (-) [350.00]	2.06 (0.00) [0]
47	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	6/2016	8/2019 (-) [12/2020]	423.00 (-) [423.00]	363.66 (0.00) [16]
48	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (-) [6/2020]	543.91 (-) [682.90]	71.46 (138.99) [4]
49	INDMAX PROJECT AT BONGAIGAON REFINERY	2/2016	11/2019 (-) [2/2020]	2,582.00 (-) [2,582.00]	1,704.47 (0.00) [3]
50	NUMALIGARH REFINERY EXPANSION PROJECT	1/2019	10/2024 (-) [10/2024]	22,594.00 (-) [22,594.00]	43.00 (0.00) [0]
51	PIPELINE NETWORK PROJECT GELEKI, ASSAM	7/2016	5/2020 (-) [5/2020]	249.85 (265.49) [265.49]	152.67 (15.64) [0]
52	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	9/2012	3/2015 (-) [0/0]	871.35 (-) [1,200.00]	565.63 (328.65) [0]
	Railways				
53	AMBARI FALAKATA TO NEW MAYNAGURI	4/2011	3/2019 (-) [3/2020]	314.00 (728.00) [728.00]	731.27 (414.00) [12]
54	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-) [3/2020]	2,232.32 (-) [2,182.00]	765.94 (-50.32) [-24]

55	DIGARU-HOJAI (102 KM)	4/2015	3/2021 (-) [3/2021]	870.96 (-) [2,136.01]	610.95 (1,265.05) [0]
56	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [3/2020]	385.20 (1,532.00) [1,532.00]	652.15 (1,146.80) [12]
	Road Transport And Highways				
57	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (-) [0/0]	268.08 (-) [268.08]	203.15 (0.00) [0]
58	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	11/2010	2/2011 (-) [0/0]	470.20 (-) [630.36]	386.98 (160.16) [0]
59	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS	12/2015	12/2018 (-) [0/0]	225.02 (-) [159.20]	26.00 (-65.82) [0]
60	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	12/2015	6/2018 (-) [0/0]	223.30 (-) [223.30]	84.69 (0.00) [0]
61	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-) [0/0]	520.01 (-) [520.01]	56.63 (0.00) [0]
62	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [0/0]	588.95 (-) [588.95]	403.00 (0.00) [0]
63	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [0/0]	289.99 (-) [289.99]	15.37 (0.00) [0]
64	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (12/2021) [0/0]	252.00 (-) [252.00]	11.04 (0.00) [0]
65	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	6/2018 (12/2020) [12/2021]	437.39 (-) [437.39]	10.01 (0.00) [42]
66	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	1/2016 (2/2019) [4/2021]	294.17 (-) [294.17]	76.25 (0.00) [63]
67	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	4/2010 (-) [7/2019]	217.61 (-) [360.84]	454.21 (143.23) [0]
68	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM	11/2010	2/2014 (-) [12/2019]	197.37 (-) [197.37]	88.86 (0.00) [0]
69	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	5/2008 (-) [6/2019]	160.00 (-) [167.98]	223.81 (7.98) [0]
70	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52	6/2016	1/2019 (-) [0/0]	829.00 (-) [829.00]	311.84 (0.00) [0]
71	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [0/0]	168.39 (-) [168.39]	84.69 (0.00) [0]
72	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE	10/2017	/ (-) [6/2020]	818.00 (-) [818.00]	63.08 (0.00) [-]
73	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5	6/2015	6/2018 (1/2021) [12/2021]	463.49 (-) [463.49]	26.15 (0.00) [42]
74	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	3/2015	1/2016 (-) [0/0]	829.00 (-) [829.00]	311.86 (0.00) [0]

75	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (5/2020) [12/2020]	454.89 (-) [454.89]	141.83 (0.00) [31]
76	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	2/2009 (7/2019) [7/2019]	280.00 (520.00) [520.00]	492.41 (240.00) [0]
77	HARANGAJO TO MAIBANG, NH-54	12/2003	7/2009 (10/2018) [10/2018]	196.00 (655.17) [655.17]	655.17 (459.17) [0]
78	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008 (1/2011) [8/2013]	155.04 (255.23) [255.23]	251.39 (100.19) [0]
79	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	4/2009 (3/2011) [8/2019]	199.81 (340.14) [340.14]	319.96 (140.33) [0]
80	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008 (7/2011) [1/2014]	167.64 (435.78) [435.78]	427.96 (268.14) [0]
81	NALBARI T BIJNI (AS-7)	12/2003	4/2008 (-) [3/2020]	208.00 (-) [230.00]	340.21 (22.00) [143]
82	NALBARI TO BIJNI (AS-6)	12/2003	6/2008 (-) [9/2019]	225.00 (-) [225.00]	328.47 (0.00) [0]
83	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST	3/2017	/ (-) [0/0]	1,049.51 (-) [1,049.51]	89.16 (0.00) [0]
84	SONAPUR TO GUWAHTI (AS-3)	12/2003	3/2008 (-) [8/2020]	245.00 (-) [174.34]	225.65 (-70.66) [149]
85	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ	11/2014	2/2018 (-) [0/0]	218.31 (-) [307.47]	263.85 (89.16) [0]
86	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN	9/2018	9/2021 (-) [9/2021]	160.00 (-) [160.00]	0.50 (0.00) [0]
	<u>MANIPUR</u>				
	<u>Power</u>				
87	LOKTAK D/S HEP(NHPC)	12/1999	6/2006 (-) [0/0]	578.62 (-) [578.62]	0.00 (0.00) [0]
	<u>Railways</u>				
88	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (-) [3/2022]	4,454.17 (13,809.00) [12,524.00]	9,599.02 (8,069.83) [132]
	<u>Road Transport And Highways</u>				
89	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260.	10/2016	11/2020 (-) [11/2020]	235.31 (-) [235.31]	97.25 (0.00) [0]
90	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	8/2017	10/2018 (-) [10/2021]	517.57 (-) [457.77]	137.04 (-59.80) [36]
	<u>Urban Development</u>				
91	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	2/2014	3/2015 (-) [10/2020]	216.69 (-) [216.69]	52.00 (0.00) [67]
	<u>MEGHALAYA</u>				
	<u>Health And Family Welfare</u>				
92	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (-) [7/2020]	363.99 (-) [363.99]	219.50 (0.00) [26]

	<u>Human Resource Development</u>				
93	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	9/2013	9/2014 (-) [12/2020]	484.32 (-) [626.26]	0.00 (141.94) [75]
	<u>Railways</u>				
94	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [3/2021]	906.46 (-) [6,000.60]	263.12 (5,094.14) [0]
	<u>Road Transport And Highways</u>				
95	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	3/2019	5/2019 (-) [0/0]	306.28 (-) [306.28]	53.09 (0.00) [0]
96	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	12/2015	5/2018 (3/2018) [10/2019]	479.20 (-) [479.20]	712.89 (0.00) [0]
97	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	/ (-) [9/2021]	553.51 (-) [553.51]	44.39 (0.00) [-]
	<u>Urban Development</u>				
98	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR	4/2014	9/2017 (-) [0/0]	151.33 (-) [151.33]	7.15 (0.00) [0]
	<u>MIZORAM</u>				
	<u>Railways</u>				
99	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (3/2022) [3/2022]	2,393.47 (4,968.00) [5,021.45]	3,183.01 (2,627.98) [96]
	<u>Road Transport And Highways</u>				
100	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (12/2020) [6/2020]	195.04 (-) [377.99]	312.41 (182.95) [116]
101	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	9/2014 (6/2020) [6/2020]	186.96 (-) [305.61]	279.13 (118.65) [69]
102	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (6/2021) [6/2021]	193.69 (-) [327.92]	258.71 (134.23) [128]
103	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	519.09 (-) [519.09]	22.52 (0.00) [0]
104	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	404.29 (-) [404.29]	0.00 (0.00) [0]
105	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	640.07 (-) [640.07]	0.00 (0.00) [0]
106	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	473.18 (-) [473.18]	0.00 (0.00) [0]
107	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	518.53 (-) [518.53]	0.00 (0.00) [0]
108	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	642.96 (-) [642.96]	0.00 (0.00) [0]
109	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	537.82 (-) [537.82]	0.00 (0.00) [0]
110	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	428.11 (-) [428.11]	0.00 (0.00) [0]

111	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (12/2020) [12/2020]	624.41 (-) [992.67]	886.01 (368.26) [117]
	NAGALAND				
	Railways				
112	DIMAPUR-TIZIT NL	4/2013	3/2020 (-) [3/2020]	4,274.00 (-) [4,274.00]	0.00 (0.00) [0]
113	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015 (-) [10/2021]	2,326.52 (-) [5,806.81]	876.09 (3,480.29) [79]
	Road Transport And Highways				
114	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018 (5/2019) [0/0]	239.30 (174.70) [174.70]	9.17 (-64.60) [0]
115	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	3/2018	9/2018 (-) [0/0]	285.68 (-) [285.68]	9.58 (0.00) [0]
116	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	3/2018	9/2018 (11/2018) [0/0]	282.98 (192.60) [192.60]	24.57 (-90.38) [0]
117	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018 (-) [8/2020]	387.00 (-) [387.00]	145.18 (0.00) [23]
118	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	9/2018 (-) [0/0]	500.09 (336.49) [336.49]	0.00 (-163.60) [0]
119	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN	3/2017	11/2020 (-) [11/2020]	217.35 (-) [217.35]	35.10 (0.00) [0]
120	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683	2/2017	4/2017 (-) [0/0]	507.68 (-) [507.68]	129.13 (0.00) [0]
121	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (7/2019) [0/0]	339.57 (233.35) [233.35]	10.15 (-106.22) [0]
122	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	3/2018	9/2018 (-) [0/0]	315.03 (-) [315.03]	18.60 (0.00) [0]
123	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	9/2018 (-) [0/0]	240.64 (-) [240.64]	25.98 (0.00) [0]
124	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [0/0]	215.12 (-) [215.12]	29.88 (0.00) [0]
125	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	9/2018 (-) [0/0]	215.79 (-) [215.79]	16.54 (0.00) [0]
126	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [0/0]	272.89 (-) [272.89]	0.00 (0.00) [0]
127	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	3/2018	9/2018 (-) [0/0]	323.98 (-) [323.98]	0.00 (0.00) [0]
128	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0	3/2018	9/2018 (11/2018) [0/0]	251.97 (160.10) [251.97]	18.67 (0.00) [0]
129	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (11/2018) [0/0]	237.72 (136.73) [237.72]	45.85 (0.00) [0]
130	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM	3/2016	8/2016	373.07	216.07

	DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1		(-) [3/2020]	(387.00) [387.00]	(13.93) [43]
131	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2016 (-) [6/2020]	396.52 (339.55) [339.55]	237.99 (-56.97) [46]
132	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	3/2016	8/2016 (-) [3/2020]	429.52 (340.00) [340.00]	189.88 (-89.52) [43]
133	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M	11/2016	9/2019 (-) [0/0]	336.25 (-) [336.25]	62.64 (0.00) [0]
134	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (-) [12/2020]	172.63 (-) [172.63]	77.30 (0.00) [0]
135	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (-) [12/2020]	167.62 (-) [167.62]	61.37 (0.00) [0]
136	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA	12/2010	2/2011 (-) [0/0]	1,296.00 (-) [1,296.00]	0.00 (0.00) [0]
137	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH-	3/2019	12/2022 (-) [12/2022]	237.51 (-) [237.51]	0.00 (0.00) [0]
	<u>SIKKIM</u>				
	<u>Railways</u>				
138	SEVOK RANGPO, NEFR	4/2008	12/2015 (-) [0/0]	1,339.48 (-) [4,084.69]	332.23 (2,745.21) [0]
	<u>Road Transport And Highways</u>				
139	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	1/2013	2/2013 (-) [12/2019]	182.28 (-) [269.14]	185.49 (86.86) [0]
140	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	4/2013	8/2013 (-) [12/2019]	151.59 (240.58) [151.59]	196.76 (0.00) [0]
141	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM.	4/2013	8/2013 (-) [0/0]	166.27 (-) [166.27]	141.31 (0.00) [0]
142	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	3/2017	/ (-) [0/0]	375.80 (-) [375.80]	77.39 (0.00) [0]
143	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	11/2017	11/2017 (-) [0/0]	290.05 (-) [290.05]	54.13 (0.00) [0]
144	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA	4/2017	11/2017 (-) [0/0]	318.42 (-) [318.42]	66.63 (0.00) [0]
145	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	3/2018	6/2018 (-) [0/0]	264.84 (-) [264.84]	0.00 (0.00) [0]
146	RHENOK-RORATHANG-PAKYONG ON NH 717A	4/2017	10/2017 (-) [0/0]	388.00 (-) [447.37]	155.85 (59.37) [0]
	<u>TRIPURA</u>				
	<u>Civil Aviation</u>				
147	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	9/2015	6/2019 (-) [0/0]	338.93 (-) [339.00]	213.50 (0.07) [0]
	<u>Railways</u>				
148	AGARTALA-AKHAURA NL	4/2012	3/2020 (9/2021)	569.63 (670.00)	82.81 (100.37)

			[9/2021]	[670.00]	[18]
	Road Transport And Highways				
149	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S	10/2014	3/2018 (12/2019) [0/0]	369.00 (-) [369.00]	319.05 (0.00) [0]
150	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C	10/2016	8/2020 (-) [8/2020]	171.90 (-) [171.90]	23.19 (0.00) [0]
	Urban Development				
151	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	3/2007	12/2015 (-) [0/0]	149.73 (173.00) [175.94]	176.65 (26.21) [0]
152	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016 (-) [0/0]	202.61 (227.00) [227.00]	199.95 (24.39) [0]
153	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	12/2016 (-) [0/0]	175.49 (206.71) [206.71]	141.28 (31.22) [0]
	Total			1,05,062.97 (38,234.12) [1,51,322.72]	59,173.92 (46,259.75)
