


दलुनह; {k= dh ifj;kt ukvk
CENTRAL SECTOR PROJECTS

**₹150 djkM vkj vf/kd ykxr okyh
(₹ 150 Crore and above)**

**357oh ¶Yk'k fj ikV@357th Flash Report
t [ykb] 2015@July, 2015**

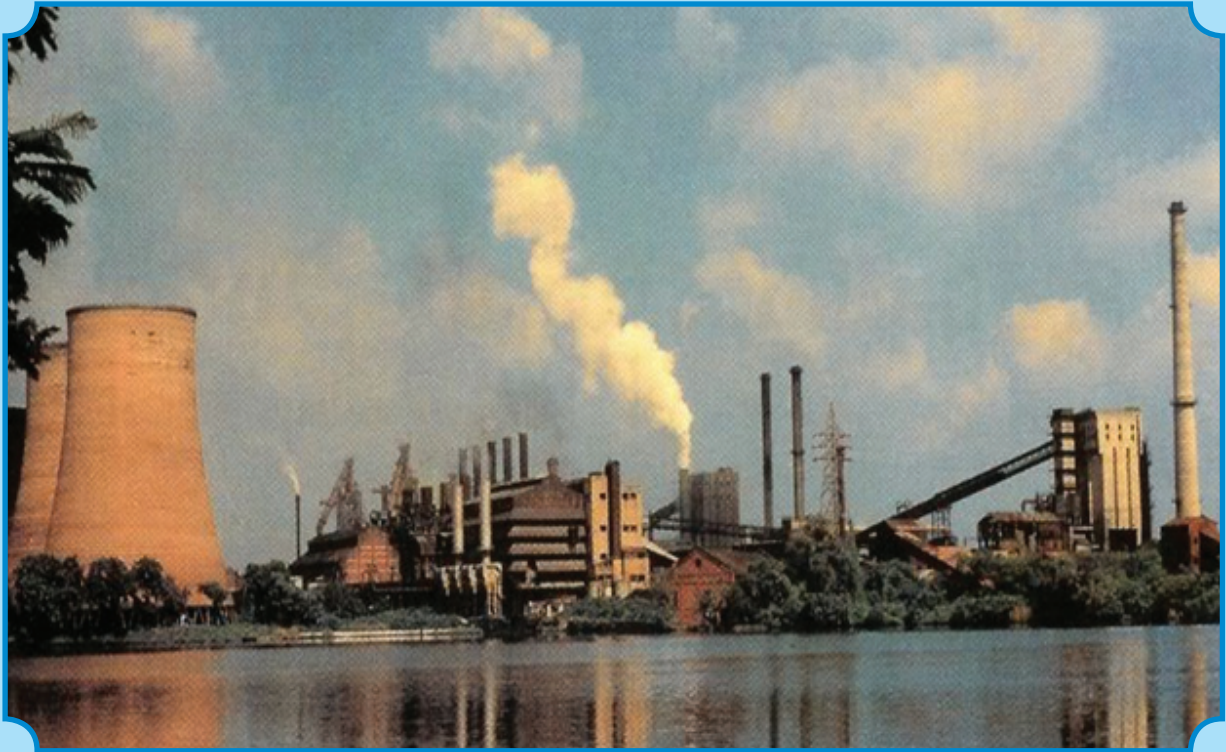

Hkkjr ljdkj / **Government of India**
lkf[;dh vkj dk;Øe dk;kUo;u e=ky;
Ministry of Statistics and Programme Implementation
vk/kkjh ljpuk vkj ifj;kt uk i=ck/ku iHkkx
Infrastructure and Project Monitoring Division
l jnkj iV;y Hkou] lln ekx]
Sardar Patel Bhavan, Sansad Marg,
ub] fnYyh / New Delhi-110001
oc lkbV / **Website- www.cspm.gov.in**

Abbreviations

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NGN	Next Generation Network
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECF	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vaccum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

Contents

	Pages
Executive Summary Hindi	1-21
Executive Summary English	22-37
Month wise List of Completed Projects Costing Rs. 150 crore and above during 2014-2015	38-39
Month wise List of Deleted Projects Costing Rs. 150 crore and above during 2014-2015	40-40
Summary of projects	41-54
Graphical Presentation of All Projects	55-66
Sector wise Analysis of Projects	67-103
Sector wise Graph	104-116
Annexures	117-117
Status of central sector projects costing Rs.150 Crore and above	118-118
List of projects in which expenditure is more than approved cost	119-124
Details of Projects Ahead of Schedule w.r.t. Original Schedule	125-125
Details of On Schedule Projects w.r.t. Original Schedule	126-132
Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule	133-144
Details of Delayed Projects w.r.t. Original and Revised Schedule	145-170
Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule	171-175
Details of Projects Without Date of Commissioning	176-191
Details of projects without original Date of Commissioning	192-193
Details of Central Sector Projects Showing Time overruns of 6 Months and More	194-204
Details of Central Sector Projects Showing Cost overruns of More Than Rs. 100 Crore	205-213
Details Of Central Sector Projects Showing Time Overruns Of 6 Months and More and cost overruns of Rs. 100 Crore	214-218
List of Projects Ahead of Schedule w.r.t. Latest Schedule	219-219
List of Projects on schedule w.r.t. Latest Schedule	220-228
List of ongoing projects having cost overrun w.r.t. to revised schedule	229-238
List of Delayed Projects w.r.t. Latest Schedule	239-250
List of Road Sector projects Implemented by NHAI as on 31-07-15 for which date of commissioning has expired/lapsed.	251-253
List of Road Sector projects Implemented by NHAI as on 31-07-15 for which cumulative expenditure has been reported zero	254-256

कार्यकारी सारांश

1. जुलाई, 2015 की फ्लैश रिपोर्ट में ₹ 150 करोड़ और उससे अधिक लागत वाली केन्द्रीय क्षेत्र की 767 अवसंरचनात्मक परियोजनाओं की स्थिति दी गई है। जुलाई 2015 के दौरान, 5 परियोजनाओं (पोत परिवहन एवं पत्तन में 2 परियोजनाएं, इस्पात, विद्युत तथा पेट्रोलियम क्षेत्र प्रत्येक में 1 परियोजना) के पूरा होने की सूचना दी गई है।

2. संदर्भाधीन माह के दौरान, 767 परियोजनाओं में से, 233 परियोजनाओं में मूल समय-सारणी की तुलना में विलंब हुआ तथा 20 परियोजनाओं के संबंध में पिछले माह में सूचित की गई समापन की तारीख की तुलना में अतिरिक्त विलंब की सूचना दी गई है। इन 20 परियोजनाओं में से, 12 परियोजनाएं ₹ 1000 करोड़ और अधिक लागत वाली बड़ी परियोजनाएं हैं।

क्र.सं.	क्षेत्र	निगरानी के तहत आने वाली परियोजनाएं (सं.)	मूल समय-सारणी की तुलना में विलंबित परियोजनाएं (सं.)	रिपोर्ट वाले माह के दौरान अतिरिक्त विलंबित परियोजनाएं (सं.)	अतिरिक्त विलंबित बड़ी परियोजनाएं (सं.)
1.	रेलवे	296	31	0	0
2.	सड़क परिवहन एवं राजमार्ग	137	21	1	0
3.	विद्युत	109	59	10	7
4.	पेट्रोलियम	70	42	3	2
5.	कोयला	77	44	3	2
6.	शहरी विकास	30	13	1	1
7.	इस्पात	25	12	1	0
8.	नागर विमानन	7	3	1	0
9.	पोत परिवहन एवं पत्तन	6	1	0	0
10.	परमाणु ऊर्जा	4	4	0	0
11.	दूरसंचार	2	1	0	0
12.	उर्वरक	1	0	0	0
13.	खदान	1	0	0	0
14.	पेट्रोरसायन	1	1	0	0
15.	भारी उद्योग	1	1	0	0
कुल		767	233	20	12

3. 767 परियोजनाओं के कार्यान्वयन की कुल मूल लागत ₹ 10,55,580.91 करोड़ थी तथा उनके पूरा होने की अनुमानित लागत ₹ 12,62,000.07 करोड़ होने की संभावना है, जो ₹ 2,06,419.16 करोड़ (मूल लागत का 19.56%) की समग्र लागत वृद्धि को दर्शाता है। जुलाई, 2015 तक इन परियोजनाओं पर किया गया व्यय ₹ 4,99,450.58 करोड़ है, जो परियोजनाओं की अनुमानित लागत का 39.58% है।

लागतवृद्धि की अधिकतम प्रतिशतता वाली परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई हैं:-

**लागतवृद्धि की अधिकतम प्रतिशतता वाली (अधिकतम संख्या में पांच) परियोजनाओं की क्षेत्र-वार सूची
(31.07.2015 की स्थिति के अनुसार)**

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (करोड़ रु.)	अनुमानित लागत(करोड़ रु.)	लागत वृद्धि(%)
परमाणु ऊर्जा					
1	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर (भाविति, 500 एम डब्ल्यू ई)	09/2003	3492.00	5677.00	62.57
2	कुडनकुलम ए पी पी (एन पी सी आई एल)	12/2001	13171.00	17270.00	31.12
नागर विमानन					
3	विभिन्न हवाई अड्डों पर सं.56 एयर फील्ड फायर निविदाओं की आपूर्ति	10/2012	217.60	244.10	12.18
4	चंडीगढ़ अंतर्राष्ट्रीय हवाई अड्डे का विकास (मोहाली) फेज-II	02/2011	452.00	489.00	8.19
कोयला					
5	अदरियाला शाफ्ट परियोजना	12/2009	212.34	1228.39	478.50
6	टीपीएस-II विस्तार (1470 मेगावाट से 1970 मेगावाट) (एनएलसी)	10/2004	2030.78	3583.77	76.47
7	तूतीकोरिन ताप विद्युत परियोजना 2X500 मेगावाट	05/2008	4904.54	6602.74	34.63
8	अमलाई ओसी विस्तार, सेक्टर-बी (1.50 एमटीवाई)	11/2009	150.59	198.59	31.87
9	मनुगुरु ओसी परियोजनाओं के आरएफआर	11/2012	430.45	486.27	12.97
भारी उद्योग					
10	राष्ट्रीय औटोमोटिव टेस्टिंग तथा आरडी अव संरचना परियोजना (एन एटी आर आई पी)	04/2011	1718.00	3827.30	122.78
पेट्रोरसायन					
11	असम गैस क्रैकर प्रोजेक्ट	04/2006	5460.61	9833.52	80.08

	पेट्रोलियम				
12	जी1 और जी एस-15 का विकास (ओ एन जी सी एल)	04/2003	429.82	3955.21	820.20
13	विजाग में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	672.00	1178.35	75.35
14	पादुर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	993.00	1693.00	70.49
15	मंगलौर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	732.00	1227.00	67.62
16	कोरबा में विपणन टी ओ पी	01/2011	141.86	232.00	63.54
	विद्युत				
17	तुरीअल जल विद्युत परियोजना (60 मेगा.)	07/1998	368.72	1381.71	274.73
18	कामेंग जल विद्युत परियोजना (नीपको)	12/2004	2496.90	6476.34	159.38
19	पारे जल विद्युत परियोजना	12/2008	573.99	1487.49	159.15
20	सुबनसिरी लोअर एच.ई.पी. (8X250 मेगा.) (एन एच पी सी)	09/2003	6285.33	15300.00	143.42
21	त्रिपुरा गैस आधारित विद्युत परियोजना	07/2009	421.01	1007.68	139.35
	रेलवे				
22	इकलाखी-बालुरघाट सहित गाजोल-इटाहार से नई बीजी रेलवे लाइन (एनएल), एन ई एफ आर	04/1983	36.80	1336.57	3531.98
23	बांकुरा-दामोदर (जीसी) (एस ई आर)	03/1998	111.90	2371.85	2019.62
24	अकोला-खांडवा जीसी अकोला-अकोट	04/2008	184.26	2000.00	985.42
25	बंगलौर-सत्य मंगलम (एन एल) (एस ब्ल्यू आर)	04/1996	138.00	1382.78	902.01
26	तिरुचिरापल्लई-नागोरे-करायकल (एसआर) (जीसी)	09/1995	100.00	980.00	880.00
	सड़क परिवहन एवं राजमार्ग				
27	पानीपत-जालंधर छः लेन (96 किमी. से 387.1 किमी.)	05/2009	1108.00	2288.00	106.50
28	मैबंग से लुमडिंग (ए एस-25), 83.400 किमी. से 111.000 किमी.	12/2003	199.81	385.13	92.75
29	मैबंग से लुमडिंग, (ए एस-24) 111.000 किमी. से 126.450 किमी.	12/2003	155.04	280.13	80.68
30	हरंगाजो से मैबंग, एन एच-54	12/2003	196.00	331.23	68.99
31	ब्रह्मपुत्र पुल एनएच सं.-31	12/2003	217.61	309.56	42.25

पोत परिवहन एवं पत्तन					
32	मुंबई में ऑफशोर कंटेनर बर्थ का निर्माण तथा बीओटी आधार पर कंटेनर टर्मिनल का विकास	01/2007	366.39	669.46	82.72
33	कोचीन पोर्ट्स के बल्लापाडम में आसीटीटी के लिए रेल कनेक्टिविटी	03/2007	245.67	373.22	51.92
34	2 ऑफशोर कंटेनर बर्थ और टर्मिनल का निर्माण और विकास	11/2007	1228.00	1460.00	18.89
इस्पात					
35	सिंटर मशीनों - 1 और 2 की सुधार	12/2009	343.00	488.40	42.39
36	3 एमटी से 6.3 एमटी तक तरल इस्पात क्षमता का विस्तार (आर आई एन एल)	10/2005	8692.00	12291.00	41.41
शहरी विकास					
37	बंगलौर मेट्रो रेल परियोजना	05/2006	6395.00	11609.00	81.53

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्य पालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

4. पूर्ण रूप से लागतवृद्धि की अधिकतम प्रतिशतता वाली (अधिकतम संख्या में पांच) परियोजनाओं की क्षेत्र-वार सूची इस प्रकार हैं:-

अधिकतम लागतवृद्धि (सीओआर) वाली (अधिकतम संख्या में 5) परियोजनाओं की क्षेत्र-वार सूची
(31.07.2015 की स्थिति के अनुसार)

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (रु. करोड़ में)	अनुमानित लागत (रु. करोड़ में)	लागतवृद्धि (रु. करोड़ में)
	परमाणु ऊर्जा				
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	13171.00	17270.00	4099.00
2	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर (भाविनि, 500 एमडब्ल्यूई)	09/2003	3492.00	5677.00	2185.00
	नागर विमानन				

3	चंडीगढ़ अंतर्राष्ट्रीय हवाई अड्डे का विकास (मोहाली) फेज-II	02/2011	452.00	489.00	37.00
4	विभिन्न हवाई अड्डों पर सं. 56 एयरफील्ड फायर निविदाओं की आपूर्ति	10/2012	217.60	244.10	26.50
कोयला					
5	तूतीकोरिन ताप विद्युत परियोजना 2X500 मेगावाट	05/2008	4904.54	6602.74	1698.20
6	टीपीएस-II विस्तार (1470 मेगावाट से 1970 मेगावाट) (एनएलसी)	10/2004	2030.78	3583.77	1552.99
7	अदरियाला शाफ्ट परियोजना	12/2009	212.34	1228.39	1016.05
8	मनुगुरु ओसी परियोजना का आरएफआर	11/2012	430.45	486.27	55.82
9	अमलाई ओसीपी विस्तार सेक्टर बी (1.50 एमटीवाई)	11/2009	150.59	198.59	48.00
भारी उद्योग					
10	राष्ट्रीय औटोमोटिव टेस्टिंग तथा आरडी अवसंरचना परियोजना (एनएटीआरआईपी)	04/2011	1718.00	3827.30	2109.30
पेट्रोरसायन					
11	असम गैस क्रैकर परियोजना	04/2006	5460.61	9833.52	4372.91
पेट्रोलियम					
12	पारादीप रिफाइनरी परियोजना	02/2009	29777.00	34555.00	4778.00
13	जी1 और जी एस-15 का विकास (ओएनजीसीएल)	04/2003	429.82	3955.21	3525.39
14	समेकित रिफाइनरी विस्तार परियोजना	03/2012	14225.00	16504.00	2279.00
15	बेसिन क्षेत्र का एकीकृत विकास	12/2012	3513.07	4619.94	1106.87
16	पादुर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	993.00	1693.00	700.00
विद्युत					
17	सुबनसिरी लोअर एच.ई.पी. (8X250 मेगावाट) (एनएचपीसी)	09/2003	6285.33	15300.00	9014.67
18	बाढ़ एसटीपीपी (3X660मेगावाट) एनटीपीसी	02/2005	8692.97	15095.67	6402.70

19	कामेंग जल विद्युत परियोजना (नीपको)	12/2004	2496.90	6476.34	3979.44
20	पार्वती एचईपी (4X200 मेवा.) (एनएचपीसी) II	09/2002	3919.59	7818.68	3899.09
21	बाढ़ एसटीपीपीचरण -II	02/2008	7341.04	10852.46	3511.42
रेलवे					
22	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	03/1995	2500.00	19565.00	17065.00
23	जिरिबाम से इम्फाल (तुपुई)(एनएल)(एनईएफआर)	04/2003	727.56	6570.75	5843.19
24	लुमडिंग-सिलचर जिरिबाम, बदरपुर- बराईग्राम कुमारघाट राष्ट्रीय परियोजना	04/1996	1676.31	5500.00	3823.69
25	बोगीबिल तथा लिंक लाइन पर ब्रह्मपुत्र पुल, एनईएफआर	09/1997	1500.00	4996.19	3496.19
26	सीवोक रंगपो, एनईएफआर	04/2008	1339.48	4190.00	2850.52
सड़क परिवहन एवं राजमार्ग					
27	पानीपत-जालंधर 6 लेन (96 किमी. से 387.1 किमी.	05/2009	1108.00	2288.00	1180.00
28	मैंबंग से लुमडिंग (एएस-25), 83.400 किमी. से 111.000 किमी.	12/2003	199.81	385.13	185.32
29	हरंगाजो से मैंबंग, एनएच-54	12/2003	196.00	331.23	135.23
30	मैंबंग से लुमडिंग, (एएस-24) 111.000 किमी. से 126.450 किमी. एनएच-54	12/2003	155.04	280.13	125.09
31	ब्रह्मपुत्रापुल, एनएच सं. -31	12/2003	217.61	309.56	91.95
पोत परिवहन एवं पत्तन					
32	मुंबई में बीओटी आधार पर ऑफशोर कंटेनर बर्थ का निर्माण तथा कंटेनर टर्मिनल का विकास	01/2007	366.39	669.46	303.07
33	2 ऑफशोर कंटेनर बर्थ और टर्मिनल का निर्माण और विकास	11/2007	1228.00	1460.00	232.00
34	कोचीन पोर्ट्स के बल्लापाडम में आईसीटीटी के लिए रेल कनेक्टिविटी	03/2007	245.67	373.22	127.55
इस्पात					
35	3 एमटी से 6.3 एमटी तक तरल इस्पात क्षमता का विस्तार (आरआईएनएल)	10/2005	8692.00	12291.00	3599.00
36	सिंटर मंशीन -1 और 2का सुधार	12/2009	343.00	488.40	145.40

शहरी विकास					
38	बंगलौर मेट्रो रेल परियोजना	05/2006	6395.00	11609.00	5214.00

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीयसलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

5. 767 परियोजनाओं में से, 7 परियोजनाएं समय से पहले चल रही हैं, 125 समय पर तथा 233 परियोजनाएं मूल समय-सारणी की तुलना में विलंबित हैं । तथापि, विलंबित परियोजनाओं की संख्या में 202 तक की कमी हो जाती है यदि विलंब की गणना समापन की अद्यतन समय-सारणी के आधार पर की जाती है । इसके अलावा, 29 परियोजनाएं किसी आरंभ संबंधी समय-सारणी/तारीख के बिना स्वीकृत की गई हैं तथा 373 परियोजनाओं के संबंध में न तो शुरू करने का वर्ष और न परियोजना के अनंतिम रूप से पूरा होने की अवधि सूचित की गई है । 233 विलंबित परियोजनाओं में से, 46 परियोजनाओं में 1 से 12 माह तक का विलंब हुआ, 49 परियोजनाओं में 13 से 24 महीने तक का विलंब हुआ, 85 परियोजनाओं में 25 से 60 माह तक का विलंब हुआ तथा 53 परियोजनाओं में 61 माह और उससे अधिक का विलंब हुआ । अधिकतम समयवृद्धि (टीओआर) वाली परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई हैं:-

**अधिकतम समय वृद्धि (टी ओ आर) वाली (अधिकतम संख्या में 5) परियोजनाओं की क्षेत्र-वार सूची
(31.07.2015 की स्थिति के अनुसार)**

क्र.सं.	परियोजना	अनुमोदन की तारीख	शुरू करने की मूल तारीख	शुरू करने की अनुमानित तारीख	समय वृद्धि (महीना)
परमाणु ऊर्जा					
1	कुडनकुलम ए पी पी (एन पी सी आई एल)	12/2001	12/2008	10/2015	82
2	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर (भाविनि, 500 एम डब्ल्यूई)	09/2003	09/2010	09/2016	72
3	काकरापार परमाणु ऊर्जा परियोजना-3 और 4	10/2009	12/2015	10/2017	22
4	राजस्थान परमाणु ऊर्जा परियोजना-7 और 8 (2x700 मेवा)	10/2009	12/2016	05/2018	17
नागर विमानन					
5	पाकयांग (सिक्किम) हवाई अड्डा में नए हवाई अड्डे का निर्माण	01/2009	01/2011	09/2017	80
6	विभिन्न हवाई अड्डों में 56 संख्या एयरफील्ड फायर	10/2012	03/2015	09/2015	6

	निविदाओं की आपूर्ति				
7	चंडीगढ़ राष्ट्रीय हवाई अड्डे का विकास (मोहाली) फेज-II	02/2011	03/2015	07/2015	4
कोयला					
8	बलराम ओसीपी विस्तार, एमसीएल 8.00 एमटीवाई	12/2007	03/2010	03/2017	84
9	टीपीएस-II विस्तार (1470 मेगावाट से 1970 मेगावाट) (एनएलसी)	10/2004	06/2009	07/2015	73
10	कुल्दा ओसीपी (महानदी कोलफील्ड लिमिटेड)	01/2005	03/2010	03/2016	72
11	अशोक विस्तार ओसीपी सीसीएल (10 एमटीवाई)	12/2007	03/2011	03/2017	72
12	झंझरा आर-VI सीम पी एस एल डब्ल्यू	11/2006	03/2011	03/2017	72
भारी उद्योग					
13	राष्ट्रीय औटोमोटिव टेस्टिंग तथा आर डी अव संरचना परियोजना (एन एटी आर आई पी)	04/2011	09/2011	12/2017	75
पेट्रोरसायन					
14	असम गैस क्रैकर परियोजना	04/2006	04/2012	09/2015	41
पेट्रोलियम					
15	फुलपुर-हल्दिया पाइपलाइन परियोजना चरण-I	07/2009	01/2013	12/2018	71
16	वी के पी एल उन्नयन तथा स्पर लाइन को बिछाना (भिलवाड़ा तथा चित्तौड़गढ़ के लिए)	12/2009	06/2011	03/2016	57
17	12 ऑफशोर आपूर्ति उपकरणों की निर्माण (ओ एस वी)	06/2007	09/2011	12/2015	51
18	मंगलौर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	10/2011	01/2016	51
19	पादुर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	01/2012	01/2016	48
विद्युत					
20	तुरीअल जल विद्युत परियोजना (60 मेगावाट)	07/1998	07/2006	10/2016	123
21	पार्वती एचईपी (4X200मेगावाट) (एन एच पी सी) II	09/2002	09/2009	12/2018	111
22	कैगा 3 तथा 4 पारेषण प्रणाली (पी जी सी आई एल)	03/2005	12/2007	12/2015	96
23	टेहरी पंचड भंडारण संयंत्र (1000 मेगावाट)	07/2006	07/2010	05/2018	94
24	कुडनकुलम एपीपी पारेषण प्रणाली (पी जी सी आई एल)	05/2005	09/2008	03/2016	90
रेलवे					
25	गोंडिया-जबलपुर (जीसी), (एसईसीआर)	02/1997	03/1998	12/2019	261

26	उधमपुर-श्रीनगर-बारामूला (एन एल), एनआर	03/1995	11/2002	12/2018	193
27	बांकुरा-दामोदर (जीसी) (एस ई आर)	03/1998	03/2005	12/2019	177
28	तमलुक-दीघा लाइन दोहरीकरण, (एस ई आर)	03/1984	06/2005	12/2019	174
29	बेलापुर-सीवुड-उरान विद्युतीकृत दोहरी लाइन (एम टी पी)	03/1996	03/2004	03/2016	144
सड़क परिवहन एवं राजमार्ग					
30	सोनापुर से गुवाहाटी (ए एस-3)	12/2003	03/2008	01/2016	94
31	नलबारी से बिजनी (ए एस-7)	12/2003	04/2008	01/2016	93
32	गुवाहाटी से नलबारी (ए एस-5)	12/2003	04/2008	12/2015	92
33	धरमतुल से सोनापुर, 205 किमी.-183 किमी. (ए एस-20)	12/2003	05/2008	10/2015	89
34	गुवाहाटी से नलबारी (एएस-4)	12/2003	04/2008	08/2015	88
पोत परिवहन एवं पत्तन					
35	मुंबई में ऑफशोर कंटेनर बर्थ का निर्माण तथा बी ओ टी आधार पर कंटेनर टर्मिनल का विकास	01/2007	12/2010	01/2016	61
इस्पात					
36	बोकारो इस्पात संयंत्र का विस्तार	05/2010	12/2011	08/2015	44
37	भिलाई इस्पात संयंत्र का विस्तार	08/2010	03/2013	03/2016	36
38	7.0 एम टी पी ए कुमार स्वामी लौह अयस्क खनन परियोजना (एनएमडीसी)	02/2011	05/2013	08/2015	27
39	45 एमवीए साफ्ट से जड़े दूसरी सुविधाएं	12/2011	10/2013	12/2015	26
40	कैप्टिव पावर प्लांट—2	02/2011	09/2013	07/2015	22
दूरसंचार					
41	टर्नकी आधार पर बीएसएनएल में ईआरपी कार्यान्वयन	10/2009	10/2010	09/2015	59
शहरी विकास					
42	प्रगति मैदान से सटे जमीन पर भारतीय उच्चतम न्यायालय के लिए अतिरिक्त परिसर का निर्माण	07/2012	08/2014	06/2017	34
43	संसदीय सौध संसद भवन परिसर नई दिल्ली में भवन के विस्तार हेतु निर्माण कार्य	05/2009	05/2013	11/2015	30
44	सार्वजनिक ट्रेनिंग (सीएपीटी) भोपाल के लिए सेंट्रल अकादमी का निर्माण	12/2012	12/2014	12/2016	24

45	प्लॉट नं. 4, सेक्टर- 10 द्वारिका नई दिल्ली पर पी एन बी के मुख्य कार्यालय भवन का निर्माण	05/2012	12/2014	04/2016	16
46	आई आई एस ई आर कोलकाता के लिए हरिघंटा कल्याणी में शैक्षिक सहित आवासीय परिसर	02/2014	09/2015	12/2016	15

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीयसलाहकार और अधिक समयवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

6. अप्रैल 2015 में, इस मंत्रालय की निगरानी पर चल रहे 738 परियोजनाओं में से, 238 परियोजनाओं के संबंध में लागतवृद्धि तथा 323 परियोजनाओं के संबंध में समयवृद्धि की सूचना प्राप्त हुई है; जबकि जुलाई, 2015 के दौरान, 767 परियोजनाओं में से 224 परियोजनाओं के संबंध में लागतवृद्धि तथा 233 परियोजनाओं के संबंध में समयवृद्धि की सूचना प्राप्त हुई है। अप्रैल 2015 की तुलना में, लागतवृद्धि दर्शाने वाले परियोजनाओं की संख्या 30.47% से घटकर 29.20% हो गई, जबकि समयवृद्धि दर्शाने वाले परियोजनाओं के संबंध में 42.61% से घटकर 30.38% हो गई है ।

7. विभिन्न अन्य परियोजना कार्यान्वयन एजेंसियों द्वारा यथा सूचित समयवृद्धि के संक्षिप्त कारणों में भूमि अधिग्रहण में विलंब, वन संबंधी अनुमति में विलंब, उपस्करों की आपूर्ति में विलंब, निधि की कमी, भूवैज्ञानिक गतिविधियां, उपस्कर स्थापित करने में समस्या, भूखनन की स्थिति, सिविल कार्यों में धीमी प्रगति, श्रम की कमी, ठेकेदार द्वारा अपर्याप्त संसाधन जुटाना, माओवादी समस्याएं, न्यायालय मामले, संविदात्मक मुद्दे, आरओयू/आरओडब्ल्यू समस्याएं, कानून और व्यवस्था की स्थिति, आदि शामिल हैं ।

8. मंत्रालय के ऑनलाइन कम्प्यूटरीकृत मॉनीटरिंग सिस्टम (ओसीएमएस) में विभिन्न अवसंरचना परियोजनाओं के लक्ष्यों की निगरानी की परिकल्पना की गई है । परियोजना प्राधिकारियों से नियमित रूप से अनुरोध किया गया है कि वे बेहतर निगरानी को सुचारू बनाने के लिए प्रत्येक परियोजना के संबंध में उपलब्धियों की सूची की प्रविष्टि करें । तथापि, सभी परियोजना एजेंसियां उपलब्धियों की सूची प्रदान नहीं कर रही हैं । बिना उपलब्धियों वाली पहले की परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई है:-

**बिना उपलब्धियों वाली पहले की परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची
(31.07.2015की स्थिति के अनुसार)**

क्र. सं.	परियोजनाएं	अनुमोदन की तारीख	मूल लागत (करोड़ रु.)	अनुमानित लागत (करोड़ रु.)	संचयी व्यय (करोड़ रु.)	शुरू करने की मूल तारीख	शुरू करने की अनुमानित तारीख
नागर विमानन							
1	पाकयांग (सिक्किम)हवाई अड्डा में नया हवाई अड्डा का निर्माण	01/2009	309.46	309.46	338.82	01/2011	06/2017
2	10 हवाई अड्डों में एयरपोर्ट संचालन नियंत्रण केन्द्रों की स्थापना	02/2010	344.28	344.28	58.50	03/2014	05/2015
3	चंडीगढ़ राष्ट्रीय हवाई अड्डे का विकास	02/2011	452.00	489.00	410.25	03/2015	04/2015
4	नईअंतरराष्ट्रीयटर्मिनल भवनकानिर्माण	05/2010	335.61	388.53	297.58	05/2012	03/2015
5	गगनपरियोजना	09/2008	626.00	626.00	514.70	06/2013	एनआर
कोयला							
6	मुराईदीह यूजी	02/2011	339.88	339.88	0.00	04/2014	03/2016
7	उत्तरी तीसरा और दक्षिणी तीसरा विस्तार ओसीपी (6एमटीवाई)	02/2014	555.52	555.52	0.00	03/2021	03/2021
8	अमेरा ओसी आरसीई	02/2015	335.97	335.97	30.30	03/2018	03/2018
9	अमृतधारा ओसी परियोजना	02/2015	481.60	481.60	0.00	03/2023	03/2023
10	बिजारीओसीआरसीई (1.50 एमटीवाई)	05/2014	164.49	164.49	22.10	03/2020	03/2020
उर्वरक							
11	नई सीवेज ट्रीटमेंट संयंत्र पैकेज, आरसीएफ ट्राम्बे	10/2014	197.79	197.79	13.09	11/2016	11/2016
भारी उद्योग							
12	राष्ट्रीय ऑटोमोटिव टेस्टिंग तथा आरडी अवसंरचना परियोजना	04/2011	1718.00	3827.30	0.00	09/2011	12/2017

खान							
13	मलंजखंड खान का विस्तार- भूमिगत खान का विकास	09/2011	1856.00	1856.00	0.00	09/2017	09/2017
पेट्रोलियम							
14	मंगलौर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	732.00	1227.00	944.84	10/2011	10/2015
15	पादुर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	993.00	1693.00	1398.50	01/2012	10/2015
16	विजाग में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	672.00	1178.35	1099.88	10/2011	10/2015
17	एक बहुदेशीय सहायता वेसेल्स का निर्माण	01/2010	723.64	723.64	0.00	03/2013	06/2016
18	बी-173ए क्षेत्र की विकसित तेल वसूली	01/2012	352.49	352.49	115.81	03/2014	05/2016
विद्युत							
19	बीआरबीसीएल-नबीनगर-जेवी	01/2007	5353.00	5353.00	0.00	05/2014	05/2014
20	एनपीजीसीपीएल-नबीनगर-जेवी	01/2013	12964.60	12964.60	0.00	01/2018	01/2018
21	यूआरटीडीएसएम चरण-I	01/2014	374.63	374.63	0.00	04/2016	04/2016
22	दक्षिणी क्षेत्रकोसुदृढ बनानेकीयोजना-XXII	01/2015	203.28	203.28	0.00	07/2017	07/2017
23	किशनगंगा एचईपी के साथ जुड़ी पारेषण प्रणाली	01/2015	268.80	268.80	0.00	03/2018	03/2018
रेलवे							
24	जिंद-सोनीपत (एनएल), एनआर	01/2004	238.56	740.00	639.77	03/2012	12/2012
25	लिंक्ड फिंगर के साथ-साथ रंगिया-मूरकॉगस्लेक	01/2004	915.70	3700.00	3198.30	एनआर	03/2015

26	कालीकट-मैंगलोर (डीएल) (एसआर)	02/1996	240.00	579.37	599.40	एनआर	02/2012
27	अहमदनगर-पर्ली वैजनाथ (एनएल),सीआर	02/1997	514.68	2820.00	329.67	एनआर	एनआर
28	दौसा-गंगापुर सीटी (एनएल), एनडब्ल्यूआर	02/1997	410.08	410.08	294.70	एनआर	एनआर
सड़क परिवहन एवं राजमार्ग							
29	छपरा-हाजीपुर की चार लेनिंग	01/2011	575.00	575.00	835.60	07/2013	12/2015
30	देवली-कोटा	01/2011	593.00	593.00	761.30	07/2013	04/2016
31	जोरबट-बारापानी	01/2011	536.00	536.00	0.00	01/2014	एनआर
32	कांडला-मुंदरा पोर्ट	01/2011	953.88	953.88	953.88	07/2013	06/2015
33	पीएस कानपुर कबरई की दो लेनिंग	01/2013	373.47	373.47	0.00	07/2014	एनआर
पोत परिवहन एवं पत्तन							
34	सिंगल प्वाइंट मूरिंग (एसपीएम) तथा एली की स्थापना करना	02/2011	830.00	621.53	0.00	05/2013	एनआर
35	कोचीन पोर्ट ट्रस्ट के वल्लारपदम में आईसीटीटी के लिए रेल संपर्क	03/2007	245.67	373.22	373.22	04/2009	एनआर
36	सेतुसमुद्रमशिप चैनलपरियोजना	06/2005	2427.40	2427.40	831.23	10/2008	एनआर
37	मौजूदा बर्थ एन का संशोधन करना तथा सुदृढीकरण	06/2010	277.00	277.00	0.21	03/2012	एनआर
38	एन्नौर मनाली एक्सप्रेस वे, एफ/ओ स्पेशल पर्पस व्हीकल	10/2002	150.00	600.00	139.80	03/2006	एनआर
इस्पात							
39	गैस नेटवर्क बीएसएल	03/2015	255.19	255.19	0.00	03/2018	03/2018
40	आरएसपी में नया एचएसएम	04/2015	3127.30	3127.30	0.00	04/2018	04/2018
41	सिंटर मशीनों - 1 और	12/2009	343.00	488.40	24.02	10/2016	10/2016

	2 की सुधार						
	दूरसंचार						
42	एनएफएस	03/2012	13334.00	13334.00	0.00	07/2015	07/2015
43	रक्षा क्षेत्र के टेलीकॉम नेटवर्क आवश्यकता का निष्पादन	05/2006	1077.00	1077.00	0.00	03/2009	एनआर
44	असम टेलीकॉम सर्किल, चरण-V.I, 2जीऔर3जी	06/2007	336.81	336.81	199.37	01/2009	03/2015
45	टर्नकीआधारपरबीएसएनएलमेंईआरपीकार्यान्वयन	10/2009	384.00	384.00	55.22	10/2010	09/2015
	शहरी विकास						
46	आईआईएसईआर कोलकाताके लिए हरिघंटा कल्याणी में शैक्षिक सहित आवासीय परिसर	01/2009	225.81	225.81	0.00	06/2012	06/2015
47	एनआईटी कालीकट केरल के लिए मेगा होस्टल II कानिर्माण	01/2010	165.23	165.23	0.00	10/2012	09/2013
48	आईआईटी हौज खास नई दिल्ली में लेक्चर थियेटर और लैब कॉम्प्लेक्स	01/2010	162.90	162.90	0.00	07/2012	06/2014
49	प्लॉट संख्या सी-41-4 पर आयकर विभाग के लिए कार्यालय भवन	02/2011	241.33	241.33	1.75	11/2014	12/2014
50	बिहटा, पटना आईआईटी के कैम्पस के लिए आवासीय तथा अन्य परिसर	02/2012	171.10	171.10	0.00	09/2014	एनआर

एन.आर.: सूचित नहीं

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्य तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और उपलब्धियों को अंतिम रूप देने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

9. यह भी पाया गया है कि परियोजना एजेंसियां संशोधित लागत अनुमानों तथा अनेक परियोजनाओं को शुरू करने की समय-सारणी को सूचित नहीं कर रही हैं, जो संकेत देता है कि

समय/लागत वृद्धि संबंधी आंकड़े कम बताए गए हैं। बिना संशोधित लागत अनुमानोंवाली शुरुआती (सबसे पुरानी) परियोजनाओं(अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई है:-

संशोधित लागत अनुमानों के बिना पहले की (सबसे पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची(31-07-2015 की स्थिति के अनुसार)

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (करोड़ रु. में)	संशोधित लागत(करोड़ रु. में)	संचयी व्यय (करोड़ रु. में)
	परमाणु ऊर्जा				
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	13171.00	0.00	18271.00
	नागर विमानन				
2	सी/ओ पाकयांग (सिक्किम) हवाई अड्डा में नया हवाई अड्डा	01/2009	309.46	0.00	338.82
	कोयला				
3	टीपीएस-II विस्तार (1470 मेगावाट से 1970 मेगावाट) (एनएलसी)	10/2004	2030.78	3027.59	3207.92
	पेट्रोलियम				
4	बी-193 क्लस्टर क्षेत्रों का विकास	06/2007	3248.78	5633.44	5925.40
	विद्युत				
5	बाढ़ एसटीपीपी फेज-II	02/2008	7341.04	0.00	8631.00
6	सुबनसिरी लोअर एच.ई.पी. (8X250 मेगावाट) (एनएचपीसी)	09/2003	6285.33	0.00	7687.18
7	पार्वती एचईपी (4X200मेगावाट) (एनएचपीसी) II	09/2002	3919.59	0.00	5040.21
8	किशनगंगा एचईपी (3x110 मेवा)	01/2009	3642.04	0.00	3934.97
9	छत्तीसगढ़ में आईपीपीएस जेनरेशन परियोजनाओं के लिए डब्ल्यूआर के पश्चिमी भाग में पारेषण प्रणाली का सुदृढीकरण	11/2011	2127.51	0.00	2172.33
10	तीस्ता लो डैम एचईपी चरण-IV (4X40 मेवा) (एनएचपीसी)	09/2005	1061.38	0.00	1742.55
	रेलवे				
11	उधमपुर-श्रीनगर-बारामूला (एनएल),	03/1995	2500.00	3000.00	10658.34

	एनआर				
12	लुमडिंग-सिल्चर-जिरिबम बदरपुर-बराईग्राम-कुमारघाट राष्ट्रीय परियोजना	04/1996	1676.31	0.00	4734.45
13	दमदम-नावपारा और नावपारा-एनएससीपी एयरपोर्ट तक विस्तार के साथ टॉलीगंज-गरिया (एमटीपी)	03/2000	1049.69	3385.14	3541.20
14	बोगीबिल तथा लिंक लाइनों पर ब्रह्मपुत्र पुल, एनईएफआर	09/1997	1500.00	1000.00	3410.06
15	लिंकड फिंगर्स के साथ रंगिया-मुर्कोंगसलेक एनईएफआर	01/2004	915.70	915.70	3198.30
सड़क परिवहन एवं राजमार्ग					
16	पानीपत-जालंधर छः लेनिंग (96 किमी. से 387.1 किमी.)	05/2009	1108.00	0.00	3466.00
17	नागपुर-बेतुल के चार लेनिंग	02/2011	2498.76	0.00	2786.00
18	सूरत-दहिसर (छः लेन) 263 किमी. से 502 किमी.	02/2009	1693.75	0.00	2762.00
19	गाजियाबाद-अलीगढ़एनएच-91	02/2011	1141.00	0.00	2445.00
20	मुरादाबाद-बरेली	04/2010	1267.00	0.00	2425.00
पोत परिवहन एवं पत्तन					
21	कोचीन पोर्ट्स के बल्लापाडम में आईसीटीटी के लिए रेल कनेक्टिविटी	03/2007	245.67	0.00	373.22

एन.आर.: सूचित नहीं.

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और संशोधित लागत अनुमानों को अंतिम रूप देने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

10. शुरू करने की संशोधित तारीख के बिना पहले की परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची इस प्रकार है:-

शुरू करने की संशोधित अनुसूची के बिना पहले की (पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची (31.07.2015 की स्थिति के अनुसार)

क्र. सं.	क्षेत्र/परियोजना	अनुमोदन की तारीख	शुरू करने की मूल तारीख	शुरू करने की संशोधित तारीख	शुरू करने की अनुमानित तारीख
नागर विमानन					
1	गगनपरियोजना	09/2008	06/2013	एनआर	06/2013
2	वीएस आईहवाई अड्डे, पोर्ट ब्लेयर में नए एकीकृत टर्मिनल भवन का निर्माण	10/2013	एनआर	एनआर	एनआर
कोयला					
1	शांतिखानी लॉगवॉलपरियोजना-एससीसीएल	10/2006	03/2012	एनआर	एनआर
2	जल्लारामशॉफ्टपरियोजना	09/2007	03/2013	एनआर	एनआर
3	रामागुंडमओसी॥ विस्तार	12/2009	03/2012	एनआर	एनआर
4	मुराडडीहयूजी टर्नकीपरियोजना	02/2011	04/2014	एनआर	04/2014
5	कृष्णाशिला(एनसीएल) (4एमटीवाई)	06/2011	03/2013	एनआर	03/2014
पेट्रोरसायन					
1	असम गैस क्रैकर परियोजना	04/2006	04/2012	एनआर	एनआर
पेट्रोलियम					
1	एन्नोरमेंईविपणनटर्मिनल	11/2006	एनआर	एनआर	एनआर
2	बीपीसीआर /एचपीसीआरसे उरान एलपीजी संयंत्र तक एलपीजीकेहस्तांतरणकेलिएपाइपलाइन	08/2009	08/2012	एनआर	एनआर
3	एन्नोर-त्रिची-मदुरैएलपीजीपाइपलाइन	05/2013	एनआर	एनआर	एनआर
विद्युत					
1	कैगा 3 तथा 4 पारेषण प्रणाली (पीजीसीआईएल)	03/2005	12/2007	12/2009	एनआर
2	कुनाडकुलमएपीपीट्रांसप्रणाली (पीजीसीआईएल)	05/2005	09/2008	एनआर	03/2013
3	एसआर -XII की व्यवस्था कासुदृढीकरण	02/2010	06/2012	एनआर	एनआर
4	आंध्रप्रदेशभाग-ए1 केवैमागिरीक्षेत्रमें आईएसजीएसपरियोजनाओंसेजुडीसामान्यप्रणाली	03/2012	06/2014	एनआर	एनआर

रेलवे					
1	नांगलडैम-तलवाड़ा (एनएल), एन.आर.	03/1981	07/2012	एनआर	एनआर
2	गजोली-ईटाहर(एनएल), एनईएफआरसहितएकलाखी-बालुरघाटसेनईबीजीरेलवेलाइन	04/1983	एनआर	एनआर	एनआर
3	तामलुकदीघा, लाइनदोहरीकरण (एसईआर)	03/1984	06/2005	07/2011	एनआर
4	नामखानाचंद्रनगर काकद्वीप-बुदाखाली तथा चंद्रनगर के लिए लक्ष्मीकांतपुर-नामखाना, इसके बाद एमएम	04/1987	एनआर	एनआर	एनआर
5	विरमगम-भिल्डी (डब्ल्यूआर), जीसी	04/1990	एनआर	03/2010	एनआर
सड़क परिवहन एवं राजमार्ग					
1	लखनऊ-रायबरेली	07/1999	07/2012	एनआर	09/2014
2	दीवापुरसे यूपी/बिहारसीमा (एलएमएनएचपी-9) एनएच-28, किमी.402-360.915	12/2003	10/2008	एनआर	एनआर
3	सिलिगुडी से इस्लामपुर (पश्चिमबंगाल-7)	12/2003	07/2008	एनआर	एनआर
4	नलबाडी सेबिजनी (एस-8)	12/2003	06/2008	एनआर	एनआर
5	पिंपलगांव-नासिक-गोंडी, एनएच-3 (एनएचडीपीचरणIII)	03/2005	07/2012	एनआर	07/2012
पोत परिवहन एवं पत्तन					
1	ट्यूना, कांडला पोर्ट ट्रस्ट के नजदीक टेकरा की बर्थिंग और संबंधित सुविधाओं का निर्माण	04/2005	02/2011	एनआर	12/2012
2	सेतुसमुद्रमशिपचैनलपरियोजना	06/2005	10/2008	11/2010	एनआर
3	मुम्बईहार्बरचैनल और जेएनपीटी चैनल को चौड़ा करना और मजबूत करना	10/2005	10/2008	एनआर	एनआर
4	पारादीपबंदरगाहपरचैनलका सुदृढीकरण	12/2005	एनआर	01/2009	12/2010
5	कांडलामें13 और14 कार्गोबर्थकानिर्माण	12/2005	03/2011	एनआर	03/2013
शहरी विकास					
1	सी/ओसैन्यरक्षामंत्रालयस्टेशनमामुनपंजाबमेंवैवाहिक आवासीय	08/2005	08/2007	एनआर	एनआर
2	बंगलोरमेट्रोरेलपरियोजना	05/2006	06/2011	एनआर	03/2013
3	सी/ओबांद्राकुर्लाकॉम्प्लेक्स, मुंबईमेंआईडीबीआईकेलिएकार्यालयभवन	11/2006	04/2009	एनआर	एनआर
4	सी/ओएनआईटीकालीकटकेरलकेलिएमेगाहॉस्टलII	01/2010	10/2012	एनआर	एनआर

5	आईआईटीहॉजखासनईदिल्लीमेंलेक्चर थिएटरऔरप्रयोगशालापरिसर	01/2010	07/2012	एनआर	07/2012
---	---	---------	---------	------	---------

एन.आर.: सूचित नहीं.

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और शुरू करने की संशोधित तारीख को अंतिम रूप देने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

11. अतिरिक्त विलंब का क्षेत्र-वार ब्योरा निम्नानुसार है:-

- i) **नागर विमानन क्षेत्र में**, 7 परियोजनाओं में से 3 परियोजनाएं विलंबित हैं। माह के दौरान, 1 परियोजना 'पकयोंग (सिक्किम) एयरपोर्ट पर नया एयरपोर्ट का निर्माण, एएआई' के संबंध में विपरीत मौसम की स्थिति, स्थानीय समस्याएं तथा स्थल की अनुपलब्धता के कारण 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है।
- ii) **विद्युत क्षेत्र में**, 109 परियोजनाओं में से, 59 परियोजनाएं विलंबित हैं। माह के दौरान, 10 परियोजनाओं के संबंध में 1-9 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 10 परियोजनाओं में से 7 परियोजना मेगा परियोजनाएं हैं। एक परियोजना 'उत्तर पूर्व उत्तर पूर्वीय इंटरकनेक्टर I परियोजना, पीजीसीआईएल' के संबंध में कठोर आरओडब्ल्यू समस्याएं, वन संबंधी अनुमति तथा एनईआर में बांधा के कारण 9 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 2 परियोजनाएं 'ईस्ट कोस्ट से जुड़े सामान्य पारेषण प्रणाली तथा भाग ग श्रीकाकुलम क्षेत्र में एपी में एनसीसी विद्युत परियोजनाएं, पीजीसीआईएल' तथा ईस्ट कोस्ट इनर्जी प्रा. लि. तथा एनसीसी विद्युत परियोजना लि. एनटीओए जेन. भाग-ख के साथ जुड़ी सामान्य प्रणाली, पीजीसीआईएल' के संबंध में अन्य लाइन से जुड़ी परियोजना विलंब होने, लंबित वन संबंधी अनुमति तथा पुनर्निविदा के कारण प्रत्येक में 8 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 1 परियोजना 'एकीकृत वास्तविक समय गतिशील राज्य माप चरण I, पीजीसीआईएल' के संबंध में आपूर्ति में विलंब होने के कारण 7 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 3 परियोजनाएं 'छत्तीसगढ़ में आईपीपी जेनरेशन परियोजनाओं के लिए चंबा और रायगढ़ में पुलिंग स्टेशनों की स्थापना, पीजीसीआईएल', 'छत्तीसगढ़ में आईपीपी परियोजना के लिए डब्ल्यूआर-एनआर एचवीडीसी इंटरकनेक्टर, पीजीसीआईएल' तथा 'ईस्ट कोस्ट इनर्जी प्रा. लि. से जुड़े सामान्य प्रणाली तथा एनसीसी पावर प्रोजेक्ट लि. एनटीओए जेनरेशन, भाग ख, पीजीसीआईएल' के संबंध में क्रमशः सबस्टेशनों के लिए भूमि अधिग्रहण में विलंब तथा कठोर आरओडब्ल्यू समस्याएं, वृहत वन संबंधी भागीदारी के कारण प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 2 परियोजनाएं 'विंध्याचल-IV का पारेषण प्रणाली तथा रिहंद-III जेनरेशन परियोजना, पीजीसीआईएल', ओडिशा भाग ख में चरण I जेनरेशन परियोजनाओं के लिए पारेषण प्रणाली के संबंध में वन्यजीव अभ्यारण्य संबंधी अनुमति में विलंब, वन संबंधी

अनुमति तथा कठोर आरओडब्ल्यू समस्याओं के कारण प्रत्येक में 1माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 1 परियोजना 'डब्ल्यूआर तथा एनआर (लाइन बे तथा रिएक्टर प्रावधान) के लिए सामान्य प्रणाली को सुदृढ़ करना, पीजीसीआईएल' 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना कार्यान्वित करने वाली एजेंसियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

iii) इस्पात क्षेत्र में, 25 परियोजनाओं में से 12 परियोजनाएं विलंबित हैं । माह के दौरान, 1 परियोजना माह के संबंध में अतिरिक्त विलंब की सूचना प्राप्त हुई है । परियोजना 'आरएसपी पर एसपीपी में अतिरिक्त ताप उपचार सुविधाओं की स्थापना, सेल' के संबंध में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना कार्यान्वित करने वाली एजेंसियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

iv) कोयला क्षेत्र में, 77 परियोजनाओं में से 44 परियोजनाएं विलंबित हैं । माह के दौरान, 3 परियोजनाओं के संबंध में 1-12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । 3 परियोजनाओं में से 2 परियोजनाएं मेगा परियोजनाएं हैं । परियोजना 'तूतीकोरिन ताप विद्युत परियोजना-2X500 मेवा., एनएलसी', 'अद्रियाला शाफ्ट परियोजना, एससीसीएल' तथा 'निगाही ओसी विस्तार परियोजना 10 एमटीवाई से 15 एमटीवाई, सिंगुरुली, एनसीएल' के संबंध में क्रमशः ठेकेदार द्वारा अपर्याप्त संसाधन जुटाना; लांगवाल उपकरण की आपूर्ति में विलंब पहला लांगवाल के लिए गेट रोडवेयस के जल निकास में विलंब, तथा वनभूमि के परिवर्तन में विलंब आदि के कारण क्रमशः 1 माह, 6 माह तथा 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना कार्यान्वित करने वाली एजेंसियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

v) पेट्रोलियम क्षेत्र में, 70 परियोजनाओं में से 42 परियोजनाएं विलंबित हैं । माह के दौरान, 3 परियोजनाओं के संबंध में 1-8 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । 3 परियोजनाओं में से, 2 परियोजनाएं मेगा परियोजनाएं हैं । परियोजनाएं 'वशिष्टा तथा एस-1 क्षेत्रों के एकीकृत विकास, ओएनजीसी' के संबंध में विभिन्न पैकेजों के पुनर्निविदा में देरी के कारण 8 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । परियोजना 'हीरा तथा दक्षिणी हीरा का पुनर्विकास चरण-II, ओएनजीसी' तथा 'बरोनी रिफाइनरी में कोकर ए में कोक चेम्बर्स का प्रतिस्थापन, आईओसीएल' के संबंध में क्रमशः 1 तथा 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना कार्यान्वित करने वाली एजेंसियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

vi) शहरी विकास क्षेत्र में, 30 परियोजनाओं में से, 13 परियोजनाएं विलंबित हैं । माह के दौरान, 1 परियोजना के संबंध में विलंब की सूचना प्राप्त हुई है । परियोजना 'फरीदाबाद विस्तार,

डीएमआरसीएल' के संबंध में लाइन का वाणिज्यिक संचालन शुरू करने के लिए सीएमआरएस निरीक्षण की प्रतीक्षा की बजह से 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।

- vi) सड़क परिवहन तथा राजमार्ग क्षेत्र** में से 137 में से 21 परियोजनाएं विलंबित हैं । माह के दौरान, 1 परियोजना के संबंध में विलंब की सूचना प्राप्त हुई है । परियोजना 'गुवाहाटी से नालवारी (एस-5), एनएचएआई' के संबंध में 4 माह के अतिरिक्त विलंब की सूचना प्राप्त होती है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना कार्यान्वित करने वाली एजेंसियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।
12. रेलवे मंत्रालय ने इस मंत्रालय को रेलवे द्वारा कार्यान्वित की जा रही सभी चल रही परियोजनाओं संबंधी मासिक स्थिति रिपोर्टों को प्रस्तुत करने का अभ्यास बंद कर दिया है । अतः, उपलब्ध सूचना/आंकड़े (जनवरी 2015 की स्थिति के अनुसार) का उपयोग रेलवे क्षेत्र की सभी परियोजनाओं के संबंध में किया गया है ।
 13. सड़क क्षेत्र के अंतर्गत राष्ट्रीय राजमार्ग प्राधिकरण द्वारा कार्यान्वित की गई 137 परियोजनाओं में से 98 परियोजनाएं एनएचएआई द्वारा ऑनलाईन अद्यतन किए गए हैं। इन 98 परियोजनाओं में से, 97 परियोजनाओं के लिए संचयी व्यय की सूचना शून्य के रूप में सूचित की गई है तथा 86 परियोजनाओं के संबंध में शुरू करने की संशोधित तारीख एनएचएआई द्वारा सूचित नहीं की गई है ।
 14. दिनांक 31.07.2015 की स्थिति के अनुसार, विभिन्न क्षेत्रों में ₹150 करोड़ तथा अधिक लागत वाली परियोजनाओं के संबंध में स्थिति रिपोर्ट में सूचित की गई है ।
 15. इसे सचिव, सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय का अनुमोदन प्राप्त है ।

EXECUTIVE SUMMARY

1. The Flash Report for July 2015 contains information on the status of the 767 Central Sector Infrastructure Projects costing ₹150 crore and above. During July 2015, 5 projects (2 projects in Shipping & Ports, 1 project each in Steel, Power and Petroleum sector) have reported completion.

2. During the reference month, out of 767 projects, 233 projects are delayed with respect to original schedule and 20 projects have reported additional delay vis-à-vis the date of completion reported in the previous month. Of these 20 projects, 12 are Mega Projects costing ₹ 1000 crore and above.

S.No.	Sector	Projects on monitor (No.)	Delayed Projects w.r.t original schedule (No.)	Additionally delayed during the month under report (No.)	Additionally delayed Mega Projects (No.)
1	RAILWAYS	296	31	0	0
2	ROAD TRANSPORT AND HIGHWAYS	137	21	1	0
3	POWER	109	59	10	7
4	COAL	77	44	3	2
5	PETROLEUM	70	42	3	2
6	URBAN DEVELOPMENT	30	13	1	1
7	STEEL	25	12	1	0
8	CIVIL AVIATION	7	3	1	0
9	SHIPPING AND PORTS	6	1	0	0
10	ATOMIC ENERGY	4	4	0	0
11	TELECOMMUNICATIONS	2	1	0	0
12	FERTILISERS	1	0	0	0
13	MINES	1	0	0	0
14	PETROCHEMICALS	1	1	0	0
15	HEAVY INDUSTRIES	1	1	0	0
Total		767	233	20	12

3. Total original cost of implementation of the 767 projects was ₹10,55,580.91 crore and their anticipated completion cost is likely to be ₹12,62,000.07 crore, which reflects overall cost overruns of ₹2,06,419.16 crore (19.56 % of original cost). The expenditure incurred on these projects till July 2015 is ₹4,99,450.58 crore, which is 39.58% of the anticipated cost of the projects. The sector-wise list of projects (maximum five in numbers) having maximum percentage of cost overruns is as follows:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Percentage of Cost Overruns (as on 31-7-2015)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (%)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	5677.00	62.57
2	KUDANKULAM APP (NPCIL)	12/2001	13171.00	17270.00	31.12
CIVIL AVIATION					
3	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	217.60	244.10	12.18
4	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II	02/2011	452.00	489.00	8.19
COAL					
5	ADRIYALA SHAFT PROJECT	12/2009	212.34	1228.39	478.50
6	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	10/2004	2030.78	3583.77	76.47
7	TUTICORIN THERMAL POWER PROJECT- 2X500 MW	05/2008	4904.54	6602.74	34.63
8	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	11/2009	150.59	198.59	31.87
9	RFR OF MANUGURU OC PROJECT	11/2012	430.45	486.27	12.97
HEAVY INDUSTRY					
10	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	04/2011	1718.00	3827.30	122.78
PETROCHEMICALS					
11	ASSAM GAS CRACKER PROJECT	04/2006	5460.61	9833.52	80.08
PETROLEUM					
12	DEVELOPMENT OF G1 AND GS-15 (ONGCL)	04/2003	429.82	3955.21	820.20
13	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG	01/2006	672.00	1178.35	75.35
14	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	70.49
15	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	01/2006	732.00	1227.00	67.62
16	MARKETING TOP AT KORBA	01/2011	141.86	232.00	63.54
POWER					
17	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	07/1998	368.72	1381.71	274.73
18	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	6476.34	159.38
19	PARE HYDRO ELECTRIC PROJECT	12/2008	573.99	1487.49	159.15
20	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	15300.00	143.42
21	TRIPURA GAS BASED POWER PROJECT	07/2009	421.01	1007.68	139.35
RAILWAYS					
22	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	36.80	1336.57	3531.98
23	BANKURA - DAMODAR (GC) (SER)	03/1998	111.90	2371.85	2019.62
24	AKOLA-KHANDWA GC AKOLA-AKOT	04/2008	184.26	2000.00	985.42
25	BANGLORE - SATYAMANGALAM (NL)(SWR)	04/1996	138.00	1382.78	902.01

26	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	09/1995	100.00	980.00	880.00
ROAD TRANSPORT AND HIGHWAYS					
27	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	106.50
28	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	385.13	92.75
29	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	155.04	280.13	80.68
30	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	331.23	68.99
31	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	217.61	309.56	42.25
SHIPPING AND PORTS					
32	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	82.72
33	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	245.67	373.22	51.92
34	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL	11/2007	1228.00	1460.00	18.89
STEEL					
35	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	42.39
36	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	10/2005	8692.00	12291.00	41.41
URBAN DEVELOPMENT					
37	BANGALORE METRO RAIL PROJECT	05/2006	6395.00	11609.00	81.53

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

4. The sector wise list of projects (maximum five in numbers) having maximum cost overruns (COR) in absolute term is as below:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Cost Overruns (COR)
(as on 31-7-2015)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (Rs.crore)
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	13171.00	17270.00	4099.00
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	5677.00	2185.00
CIVIL AVIATION					
3	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II	02/2011	452.00	489.00	37.00
4	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	217.60	244.10	26.50
COAL					
5	TUTICORIN THERMAL POWER PROJECT- 2X500 MW	05/2008	4904.54	6602.74	1698.20
6	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	10/2004	2030.78	3583.77	1552.99

7	ADRIYALA SHAFT PROJECT	12/2009	212.34	1228.39	1016.05
8	RFR OF MANUGURU OC PROJECT	11/2012	430.45	486.27	55.82
9	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	11/2009	150.59	198.59	48.00
HEAVY INDUSTRY					
10	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	04/2011	1718.00	3827.30	2109.30
PETROCHEMICALS					
11	ASSAM GAS CRACKER PROJECT	04/2006	5460.61	9833.52	4372.91
PETROLEUM					
12	PARADIP REFINERY PROJECT	02/2009	29777.00	34555.00	4778.00
13	DEVELOPMENT OF G1 AND GS-15 (ONGCL)	04/2003	429.82	3955.21	3525.39
14	INTEGRATED REFINERY EXPANSION PROJECT	03/2012	14225.00	16504.00	2279.00
15	INTEGRATED DEVELOPMENT OF BASSEIN FIELD	12/2012	3513.07	4619.94	1106.87
16	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	700.00
POWER					
17	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	15300.00	9014.67
18	BARH STPP(3X660MW) NTPC	02/2005	8692.97	15095.67	6402.70
19	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	6476.34	3979.44
20	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	7818.68	3899.09
21	BARH STPP STAGE -II	02/2008	7341.04	10852.46	3511.42
RAILWAYS					
22	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	19565.00	17065.00
23	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	727.56	6570.75	5843.19
24	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	04/1996	1676.31	5500.00	3823.69
25	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	09/1997	1500.00	4996.19	3496.19
26	SEVOK RANGPO, NEFR	04/2008	1339.48	4190.00	2850.52
ROAD TRANSPORT AND HIGHWAYS					
27	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	1180.00
28	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	385.13	185.32
29	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	331.23	135.23
30	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	155.04	280.13	125.09
31	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	217.61	309.56	91.95
SHIPPING AND PORTS					
32	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	303.07
33	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL	11/2007	1228.00	1460.00	232.00
34	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	245.67	373.22	127.55
STEEL					
35	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT	10/2005	8692.00	12291.00	3599.00

	(RINL)				
36	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	145.40
	URBAN DEVELOPMENT				
37	BANGALORE METRO RAIL PROJECT	05/2006	6395.00	11609.00	5214.00

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

5. Out of the 767 projects, 7 projects are ahead of schedule, 125 are on schedule and 233 are delayed with respect to their original schedule. However, the number of delayed projects decreases to 202 if delay is calculated on the basis of latest schedule of completion. Further, 29 projects have been sanctioned without original commissioning schedule date and for 373 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 233 delayed projects, 46 projects have overall delay in the range of 1 to 12 months, 49 projects have delay in the range of 13 to 24 months, 85 projects have delay in the range of 25 to 60 months and 53 projects have delay of 61 months and above. The sector wise list of projects (maximum five in numbers) having maximum time overruns (TOR) are as below:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Time Overruns (TOR)
(as on 31-7-2015)

SN	PROJECT	DOA	DOC ORIGINAL	DOC ANTICIPATED	TOR(IN MONTHS)
	ATOMIC ENERGY				
1	KUDANKULAM APP (NPCIL)	12/2001	12/2008	10/2015	82
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	09/2010	09/2016	72
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	10/2017	22
4	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	10/2009	12/2016	05/2018	17
	CIVIL AVIATION				
5	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	01/2011	09/2017	80
6	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	03/2015	09/2015	6
7	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II	02/2011	03/2015	07/2015	4
	COAL				
8	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	03/2010	03/2017	84
9	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	10/2004	06/2009	07/2015	73
10	KULDA OCP (MAHANADI COALFIELDS LTD)	01/2005	03/2010	03/2016	72
11	ASHOK EXPN OCP CCL (10 MTY)	12/2007	03/2011	03/2017	72
12	JHANJRA R-VI SEAM PSLW	11/2006	03/2011	03/2017	72
	HEAVY INDUSTRY				
13	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	09/2011	12/2017	75
	PETROCHEMICALS				

14	ASSAM GAS CRACKER PROJECT	04/2006	04/2012	09/2015	41
PETROLEUM					
15	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I	07/2009	01/2013	12/2018	71
16	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH)	12/2009	06/2011	03/2016	57
17	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	06/2007	09/2011	12/2015	51
18	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	01/2006	10/2011	01/2016	51
19	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	01/2012	01/2016	48
POWER					
20	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	07/1998	07/2006	10/2016	123
21	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	09/2009	12/2018	111
22	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL)	03/2005	12/2007	12/2015	96
23	TEHRI PUMPED STORAGE PLANT(1000MW)	07/2006	07/2010	05/2018	94
24	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	05/2005	09/2008	03/2016	90
RAILWAYS					
25	GONDIA-JABALPUR(GC),(SECR)	02/1997	03/1998	12/2019	261
26	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	11/2002	12/2018	193
27	BANKURA - DAMODAR (GC) (SER)	03/1998	03/2005	12/2019	177
28	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	06/2005	12/2019	174
29	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	03/1996	03/2004	03/2016	144
ROAD TRANSPORT AND HIGHWAYS					
30	SONAPUR TO GUWAHTI (AS-3)	12/2003	03/2008	01/2016	94
31	NALBARI T BIJNI (AS-7)	12/2003	04/2008	01/2016	93
32	GUWAHATI TO NALBARI (AS-5)	12/2003	04/2008	12/2015	92
33	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	05/2008	10/2015	89
34	GUWHATI TO NALBARI (AS-4)	12/2003	04/2008	08/2015	88
SHIPPING AND PORTS					
35	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	12/2010	01/2016	61
STEEL					
36	EXPANSION OF BOKARO STEEL PLANT	05/2010	12/2011	08/2015	44
37	EXPANSION OF BHILAI STEEL PLANT	08/2010	03/2013	03/2016	36
38	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC)	02/2011	05/2013	08/2015	27
39	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES	12/2011	10/2013	12/2015	26
40	CAPTIVE POWER PLANT - 2	02/2011	09/2013	07/2015	22
TELECOMMUNICATIONS					
41	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS	10/2009	10/2010	09/2015	59
URBAN DEVELOPMENT					

42	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	07/2012	08/2014	06/2017	34
43	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI	05/2009	05/2013	11/2015	30
44	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL	12/2012	12/2014	12/2016	24
45	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI	05/2012	12/2014	04/2016	16
46	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	02/2014	09/2015	12/2016	15

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further time overruns.

6. In April 2015, out of 758 projects on the monitor of this Ministry, 231 projects reported cost overruns and 323 projects reported time overruns; while during July 2015, out of 767 projects, 224 projects reported cost overruns and 233 projects reported time overruns. In comparison to April 2015, number of projects reporting cost overruns has gone down from 30.47% to 29.20% whereas projects reporting time overruns have decreased from 42.61% to 30.38%.

7. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in forest clearance, delay in supply of equipments, fund constraints, geological surprises, problems in equipment erection, geo-mining conditions, slow progress in civil works, shortage of labour, inadequate mobilization by the contractor, maoist problems, court cases, contractual issues, ROU/ROW problems, law and order situation etc.

8. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The sector wise list of earliest projects (maximum five in numbers) without milestones is as below:-

**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Milestones
(as on 31-7-2015)**

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST ANTICIPATED (Rs. Crore)	CUMMULATIVE EXPENDITURE (Rs. Crore)	ORIGINAL DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
CIVIL AVIATION							
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	309.46	309.46	338.82	01/2011	06/2017
2	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL	02/2010	344.28	344.28	58.50	03/2014	05/2015

	CENTRES AT 10 AI						
3	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT	02/2011	452.00	489.00	410.25	03/2015	04/2015
4	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING	05/2010	335.61	388.53	297.58	05/2012	03/2015
5	GAGAN PROJECT	09/2008	626.00	626.00	514.70	06/2013	N.R.
COAL							
6	MURADIH UG	02/2011	339.88	339.88	0.00	04/2014	03/2016
7	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY)	02/2014	555.52	555.52	0.00	03/2021	03/2021
8	AMERA OC RCE	02/2015	335.97	335.97	30.30	03/2018	03/2018
9	AMRITDHARA OC PROJECT	02/2015	481.60	481.60	0.00	03/2023	03/2023
10	BIJARI OC RCE (1.50 MTY)	05/2014	164.49	164.49	22.10	03/2020	03/2020
FERTILISERS							
11	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	197.79	13.09	11/2016	11/2016
HEAVY INDUSTRY							
12	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (	04/2011	1718.00	3827.30	0.00	09/2011	12/2017
MINES							
13	EXPANSION OF MALANJKHAND MINE- DEVELOPMENT OF UNDERGROUND MIN	09/2011	1856.00	1856.00	0.00	09/2017	09/2017
PETROLEUM							
14	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	01/2006	732.00	1227.00	944.84	10/2011	10/2015
15	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	1398.50	01/2012	10/2015
16	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG	01/2006	672.00	1178.35	1099.88	10/2011	10/2015
17	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL	01/2010	723.64	723.64	0.00	03/2013	06/2016
18	IMPROVED OIL RECOVERY OF B-173A FIELD	01/2012	352.49	352.49	115.81	03/2014	05/2016
POWER							
19	BRBCL- NABINAGAR - JV	01/2007	5353.00	5353.00	0.00	05/2014	05/2014
20	NPGCPL- NABINAGAR - JV	01/2013	12964.60	12964.60	0.00	01/2018	01/2018
21	URTDSM PHASE-I	01/2014	374.63	374.63	0.00	04/2016	04/2016

22	SYSTEM STRENGTHENING IN SOUTHERN REGION – XXIII	01/2015	203.28	203.28	0.00	07/2017	07/2017
23	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP	01/2015	268.80	268.80	0.00	03/2018	03/2018
RAILWAYS							
24	JIND-SONEPAT (NL),NR	01/2004	238.56	740.00	639.77	03/2012	12/2012
25	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER	01/2004	915.70	3700.00	3198.30	N.R.	03/2015
26	CALICUT-MANGALORE (DL) (SR)	02/1996	240.00	579.37	599.40	N.R.	02/2012
27	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	02/1997	514.68	2820.00	329.67	N.R.	N.R.
28	DAUSA-GANGAPUR CITY(NL),NWR	02/1997	410.08	410.08	294.70	N.R.	N.R.
ROAD TRANSPORT AND HIGHWAYS							
29	4-LANNING OF CHAPRA-HAJIPUR	01/2011	575.00	575.00	835.60	07/2013	12/2015
30	DEOLI-KOTA	01/2011	593.00	593.00	761.30	07/2013	04/2016
31	JORBAT - BARAPANI	01/2011	536.00	536.00	0.00	01/2014	N.R.
32	KANDLA - MUNDRA PORT	01/2011	953.88	953.88	953.88	07/2013	06/2015
33	2 LANING WITH PS KANPUR KABRAI	01/2013	373.47	373.47	0.00	07/2014	N.R.
SHIPPING AND PORTS							
34	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIE	02/2011	830.00	621.53	0.00	05/2013	N.R.
35	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS	03/2007	245.67	373.22	373.22	04/2009	N.R.
36	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	2427.40	2427.40	831.23	10/2008	N.R.
37	MODIFICATION AND STRENGTHENING OF EXISTING BERTH N	06/2010	277.00	277.00	0.21	03/2012	N.R.
38	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE	10/2002	150.00	600.00	139.80	03/2006	N.R.
STEEL							
39	GAS NETWORK BSL	03/2015	255.19	255.19	0.00	03/2018	03/2018
40	NEW HSM AT RSP	04/2015	3127.30	3127.30	0.00	04/2018	04/2018
41	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	24.02	10/2016	10/2016

TELECOMMUNICATIONS							
42	NFS	03/2012	13334.00	13334.00	0.00	07/2015	07/2015
43	EXECUTION OF TELECOM NETWORK REQUIREMENT OF DEFENCE	05/2006	1077.00	1077.00	0.00	03/2009	N.R.
44	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G	06/2007	336.81	336.81	199.37	01/2009	03/2015
45	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS	10/2009	384.00	384.00	55.22	10/2010	09/2015
URBAN DEVELOPMENT							
46	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA	01/2009	225.81	225.81	0.00	06/2012	06/2015
47	C/O MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	165.23	165.23	0.00	10/2012	09/2013
48	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI	01/2010	162.90	162.90	0.00	07/2012	06/2014
49	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-4	02/2011	241.33	241.33	1.75	11/2014	12/2014
50	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA	02/2012	171.10	171.10	0.00	09/2014	N.R.

N.R.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up milestones.

9. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The sector wise list of earliest (oldest) projects (maximum five in numbers) without revised cost estimates are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Cost Estimates (as on 31-7-2015)

SN	PROJECT	DOA	COST ORIGINAL (Rs. Crore)	COST REVISED (Rs. Crore)	CUMMULATIVE EXPENDITURE (Rs. Crore)
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	13171.00	0.00	18271.00
CIVIL AVIATION					
2	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	309.46	0.00	338.82
COAL					
3	TPS-II EXPANSION (1470MW TO 1970MW)	10/2004	2030.78	3027.59	3207.92

	(NLC)				
	PETROLEUM				
4	DEVELOPMENT OF B-193 CLUSTER FIELDS	06/2007	3248.78	5633.44	5925.40
	POWER				
5	BARH STPP STAGE -II	02/2008	7341.04	0.00	8631.00
6	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	0.00	7687.18
7	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	0.00	5040.21
8	KISHANGANGA HEP (3X110 MW)	01/2009	3642.04	0.00	3934.97
9	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH	11/2011	2127.51	0.00	2172.33
10	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	09/2005	1061.38	0.00	1742.55
	RAILWAYS				
11	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	3000.00	10658.34
12	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	04/1996	1676.31	0.00	4734.45
13	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	03/2000	1049.69	3385.14	3541.20
14	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	09/1997	1500.00	1000.00	3410.06
15	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	01/2004	915.70	915.70	3198.30
	ROAD TRANSPORT AND HIGHWAYS				
16	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	0.00	3466.00
17	4 LANING OF NAGPUR-BETUL	02/2011	2498.76	0.00	2786.00
18	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	02/2009	1693.75	0.00	2762.00
19	GHAZIABAD-ALIGARH NH-91	02/2011	1141.00	0.00	2445.00
20	MURADABAD-BAREILY	04/2010	1267.00	0.00	2425.00
	SHIPPING AND PORTS				
21	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	245.67	0.00	373.22

N.R.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised cost estimates.

10. The sector wise list of earliest projects (maximum five in numbers) without revised commissioning schedule are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Commissioning Schedule (as on 31-7-2015)

SN	SECTOR/ PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	REVISED DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
	CIVIL AVIATION				
1	GAGAN PROJECT	09/2008	06/2013	NR	06/2013
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	NR	N.R.	N.R.
	COAL				

1	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	03/2012	N.R.	N.R.
2	JALLARAM SHAFT PROJECT	09/2007	03/2013	N.R.	N.R.
3	RAMAGUNDAM OC-II EXTENSION	12/2009	03/2012	N.R.	N.R.
4	MURAI DIH UG TURN-KEY PROJECT	02/2011	04/2014	N.R.	04/2014
5	KRISHNASHILA (NCL) (4MTY)	06/2011	03/2013	N.R.	03/2014
PETROCHEMICALS					
1	ASSAM GAS CRACKER PROJECT	04/2006	04/2012	N.R.	N.R.
PETROLEUM					
1	NEW MARKETING TERMINAL AT ENNORE	11/2006	N.R.	N.R.	N.R.
2	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT	08/2009	08/2012	N.R.	N.R.
3	ENNORE-TRICHY-MADURAI LPG PIPELINE	05/2013	N.R.	N.R.	N.R.
POWER					
1	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL)	03/2005	12/2007	12/2009	N.R.
2	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	05/2005	09/2008	N.R.	03/2013
3	SYSTEM STRENGTHENING -XII OF SR	02/2010	06/2012	N.R.	N.R.
4	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1	03/2012	06/2014	N.R.	N.R.
RAILWAYS					
1	NANGALDAM-TALWARA(NL),NR	03/1981	07/2012	N.R.	N.R.
2	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	N.R.	N.R.	N.R.
3	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	06/2005	07/2011	N.R.
4	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	04/1987	N.R.	N.R.	N.R.
5	VIRAMGAM-BHILDI(WR),GC	04/1990	N.R.	03/2010	N.R.
ROAD TRANSPORT AND HIGHWAYS					
1	LUCKNOW-RAIBAREILI	07/1999	07/2012	N.R.	09/2014
2	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915	12/2003	10/2008	N.R.	N.R.
3	SILIGURI TO ISLAMPUR (WB-7)	12/2003	07/2008	N.R.	N.R.
4	NALBARI TO BIJNI (AS-8)	12/2003	06/2008	N.R.	N.R.
5	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	03/2005	07/2012	N.R.	07/2012
SHIPPING AND PORTS					
1	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST	04/2005	02/2011	N.R.	12/2012
2	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	10/2008	11/2010	N.R.
3	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL	10/2005	10/2008	N.R.	N.R.

4	DEEPENING OF CHANNEL AT PARADIP PORT	12/2005	N.R.	01/2009	12/2010
5	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA	12/2005	03/2011	N.R.	03/2013
URBAN DEVELOPMENT					
1	C/O MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB	08/2005	08/2007	N.R.	N.R.
2	BANGALORE METRO RAIL PROJECT	05/2006	06/2011	N.R.	03/2013
3	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI	11/2006	04/2009	N.R.	N.R.
4	C/O MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	10/2012	N.R.	N.R.
5	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI	01/2010	07/2012	N.R.	07/2012

N.R.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised commissioning schedule.

11. The Sector-wise details of additional delays are as under:-

- i) In the **Civil Aviation Sector**, out of 7 projects, 3 projects are delayed. During the month, 1 project 'Construction of New Airport at Pakyong (Sikkim) Airport, AAI' has reported additional delay of 3 months due to adverse weather condition, local problem and non-availability of site.
- ii) In the **Power Sector**, out of 109 projects, 59 projects are delayed. During the month, 10 projects have reported additional delay in the range of 1-9 months. Out of 10 projects, 7 are mega projects. 1 project 'North-East North Eastern Interconnector I Project, PGCIL' has reported additional delay of 9 months due to severe ROW problem, forest clearance and disturbance in NER; 2 projects 'Common Transmission System Associated with East Coast and NCC Power Projects in Srikakulam Area A.P. Part-C, PGCIL' and 'Common System Associated with East Coast Energy Pvt. Ltd. and NCC Power Projects Ltd. LTOA Generation, PGCIL' have reported additional delay of 8 months each due to commissioning linked to other line, pending forest clearance and retendering; 1 project 'Unified Real Time Dynamic State Measurement Phase-I, PGCIL' has reported additional delay of 7 months due to delay in supplies; 3 projects 'Establishment of Pooling Stations at Champa and Raigarh for IPP Generatrion Project in Chattisgarh, PGCIL', 'WR-NR HVDC Interconnector for IPP Projects in Chattisgarh, PGCIL' and Common System Associated with East Coast Energy Pvt. Ltd and NCC Power Projects Ltd. LTOA Gen Part – B, PGCIL' have reported additional delay of 3 months each due to delay in land acquisition for substations and severe ROW problem, huge forest involvement respectively; 2 projects 'Transmission System of Vindhyachal – IV and Rihand – III Gen. Project PGCIL', Transmission System for Phase-I Gen Project in Orissa – Part – A, PGCIL' have reported additional delay of 1 month each due to delay

in Wildlife sanctuary clearance, forest clearance and severe ROW problem; 1 project 'System Strengthening Common for WR and NR (Line Bays and Reactor Provision), PGCIL' has reported additional delay of 1 month. (however, no specific reason has been reported by the project implementing agency for the delay in project).

- iii) In the **Steel Sector**, out of 25 projects, 12 projects are delayed. During the month, 1 project has reported additional delay. The project 'Installation of Additional Heat Treatment Facilities in SPP at RSP, SAIL' has reported additional delay of 1 month (however, no specific reason has been reported by the project implementing agency for the delay in project).
- iv) In the **Coal Sector**, out of 77 projects, 44 projects are delayed. During the month, 3 projects have reported additional delay in the range of 1-12 months. Out of 3 projects, 2 projects are mega projects. The project 'Tuticorin Thermal Power Project- 2X500 MW, NLC', 'Adriyala Shaft Project, SCCL' and 'Nigahi OC Expansion Project 10 MTY to 15 MTY, Singrauli, NCL' have reported additional delay of 1 month, 6 months and 12 months respectively due to inadequate mobilization by the contractor; delay in supply of Longwall equipment, delay in drainage of gate roadways for Ist Longwall and delay in diversion of forest land respectively.
- v) In the **Petroleum Sector**, out of 70 projects, 42 projects are delayed. During the month, 3 projects have reported additional delays in the range of 1-8 months. Out of 3 projects, 2 projects are mega project; the project 'Integrated Development of Vashista and S-1 Fields, ONGC' has reported additional delay of 8 months due to retendering of various packages. The project 'Heera and South Heera Redevelopment Ph-II, ONGC' and 'Replacement of Coke Chambers in Coker A at Barauni Refinery, IOCL' have reported additional delay of 1 month and 2 months respectively. (however, no specific reasons have been reported by the project implementing agencies for the delay in project).
- vi) In the **Urban Development Sector**, out of 30 projects, 13 projects are delayed. During the month, 1 project has reported additional delay. The Project 'Faridabad Extension, DMRCL' has reported additional delay of 3 months due to awaited CMRS inspection for starting the commercial operation of line.
- vii) In the **Road Transport & Highways Sector**, out of 137 projects, 21 projects are delayed. During the month, 1 project has reported additional delay. The Project 'Guwhati to Nalbari (AS-5), NHAI' has reported additional delay of 4 months. (however, no specific reason has been reported by the project implementing agency for the delay in project).

12. Ministry of Railway has **discontinued** the practice of furnishing monthly status reports on all on-going projects being implemented by Railways to this Ministry. Therefore, the


available information/data (**as on January 2015**) has been used in respect of all projects of Railways sector.

13. Out of 137 projects being implemented by NHAI under the Road Sector, 98 have been updated online by the NHAI. Out of these 98 projects, the cumulative expenditure for 97 projects has been reported as **zero** and in case of 86 projects the revised date of commissioning has not been reported by the NHAI.
14. The status as on 31.07.2015 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.
15. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

EXECUTIVE SUMMARY

Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	296	0
2	ROAD TRANSPORT AND HIGHWAYS	137	1
3	POWER	109	10
4	COAL	77	3
5	PETROLEUM	70	3
6	URBAN DEVELOPMENT	30	1
7	STEEL	25	1
8	CIVIL AVIATION	7	1
9	SHIPPING AND PORTS	6	0
10	ATOMIC ENERGY	4	0
11	TELECOMMUNICATIONS	2	0
12	FERTILISERS	1	0
13	MINES	1	0
14	PETROCHEMICALS	1	0
15	HEAVY INDUSTRY	1	0
	Total	767	20

Sectoral break up of on-going infrastructure projects

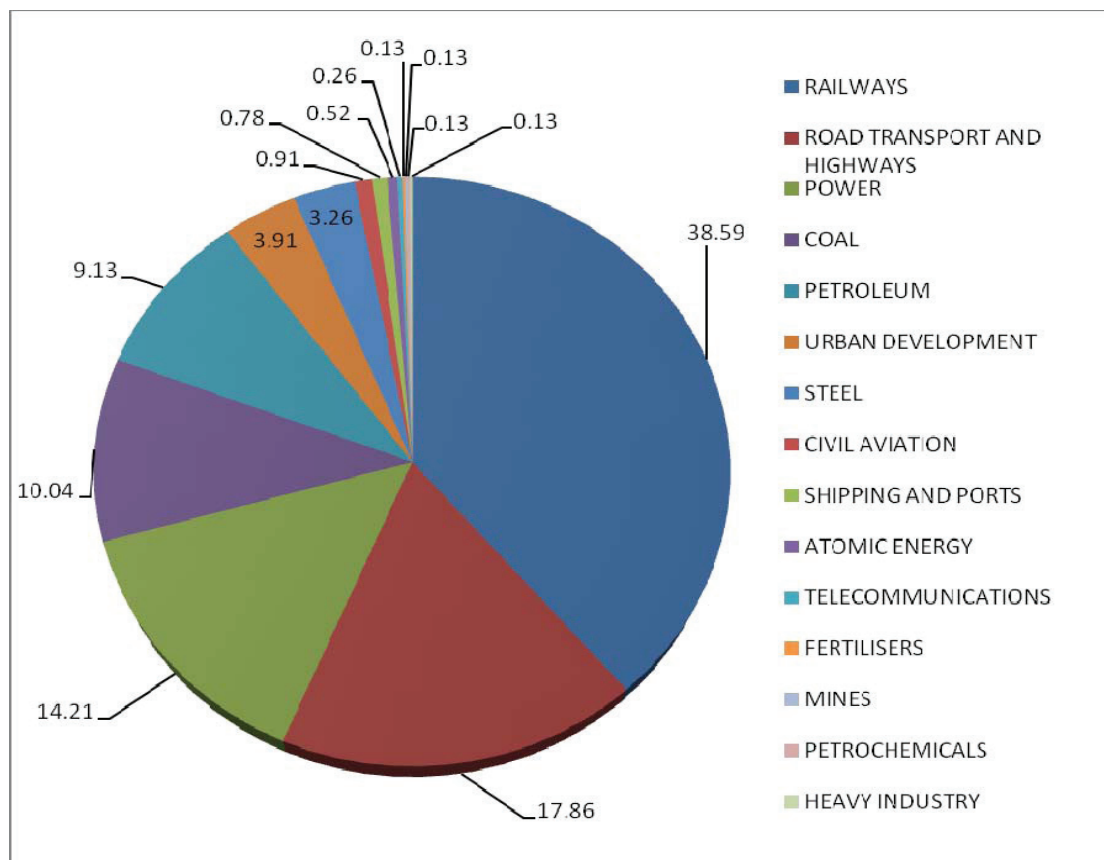

Month wise List of Completed Projects Costing Rs.150 crore and above during 2015-16				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
April,2015				
	<u>PETROLEUM</u>			
1	KOTA JOBNER PIPELINE PROJECT (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000170]	276.26	12/2015	241.63
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
2	PUNE-SHOLAPUR,PKG1 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000127]	1,110.00	05/2012	1,802.00
May,2015				
	<u>PETROLEUM</u>			
3	DEVELOPMENT OF B-193 CLUSTER FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000033]	3,248.78	08/2010	5,933.42
4	DEVELOPMENT OF CLUSTER-7 FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000104]	4,550.40	03/2013	2,583.55
5	PIPELINE REPLACEMENT PROJECT-3 (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000137]	2,547.26	05/2014	1,412.08
	<u>POWER</u>			
6	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000127]	901.77	08/2014	945.20
7	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000136]	803.34	03/2015	593.19
	<u>TELECOMMUNICATIONS</u>			
8	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G (BHARAT SANCHAR NIGAM LIMITED) - [N26000062]	336.81	01/2009	199.37
June,2015				
	<u>STEEL</u>			
9	EXPANSION OF DURGAPUR STEEL PLANT (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000074]	2,875.00	12/2012	2,640.00
10	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000075]	254.55	11/2013	135.89
	<u>POWER</u>			
11	KOLDAM HEP (NTPC) (NATIONAL THERMAL POWER CORPORATION) - [180100211]	4,527.15	04/2009	6,622.00
12	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000105]	1,366.34	12/2013	1,320.96
	<u>RAILWAYS</u>			
13	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) (NORTH EASTERN RAILWAY) - [220100255]	863.23	-	888.87
14	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR (NORTH EAST FRONTIER RAILWAY) - [220100315]	915.70	-	3,198.30

Month wise List of Completed Projects Costing Rs.150 crore and above during 2015-16				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
July, 2015				
	<u>STEEL</u>			
15	AUGMENTATION OF IRON ORE STORAGE IN RMHP (RASTRIYA ISPAT NIGAM LIMITED) - [N12000053]	480.00	09/2009	388.52
	<u>PETROLEUM</u>			
16	SURAT PARADIP PIPELINE PROJECT (GAS AUTHORITY OF INDIA LIMITED) - [N16000163]	10,281.00	04/2015	1.49
	<u>POWER</u>			
17	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000130]	1,263.26	11/2014	1,131.58
	<u>SHIPPING AND PORTS</u>			
18	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (PORT TRUST) - [N25000035]	150.00	03/2006	139.80
19	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS(PORT TRUST) - [N25000060]	830.00	05/2013	0.01

Month wise List of Deleted Projects Costing Rs. 150 crore and above during				
2015-2016				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
May, 2015				
	<u>PETROLEUM</u>			
1	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000170]	723.64	03/2013	.00
2	AHMEDABAD REDEVELOPMENT PROJECT (OIL & NATURAL GAS CORPORATION LIMITED) - [N24000127]	1,916.10	12/2014	1,160.14
3	MEHESANA REDEVELOPMENT PROJECT (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000033]	3,823.00	04/2015	1,076.57
4	ANKLESWAR REDEVELOPMENT (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000104]	2,189.63	12/2014	1,034.30
5	INTEGRATED DEVELOPMENT OF BASSEIN FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000137]	3,513.07	02/2016	.47
6	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS (OIL & NATURAL GAS CORPORATION LIMITED) - [N18000127]	2,913.10	05/2016	13.86
June, 2015				
7	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS (OIL & NATURAL GAS CORPORATION LIMITED) - [N18000136]	2,913.10	05/2016	13.86
8	IMPROVED OIL RECOVERY OF B-173A FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N26000062]	352.49	03/2014	122.87
	<u>TELECOMMUNICATIONS</u>			
9	EXECUTION OF TELECOM NETWORK REQUIREMENT OF DEFENCE FORCES (BHARAT SANCHAR NIGAM LIMITED) - [N12000074]	1,077.00	03/2009	.00


Summary of projects in the Flash Report for the month of July, 2015

Project Implementation - Current Status:

Number of Projects in Previous Month	770
Number of Projects completed/dropped/frozen in Current Month	5
Number of Projects Added in Current Month	2
Number of Projects in Current Month	767


Brief Analysis

Project Status with respect to Original Schedule: Out of 767 projects, 7 projects are ahead of schedule, 125 projects are on schedule 233 projects are delayed. 373 projects do not have fixed dates of commissioning. 29 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

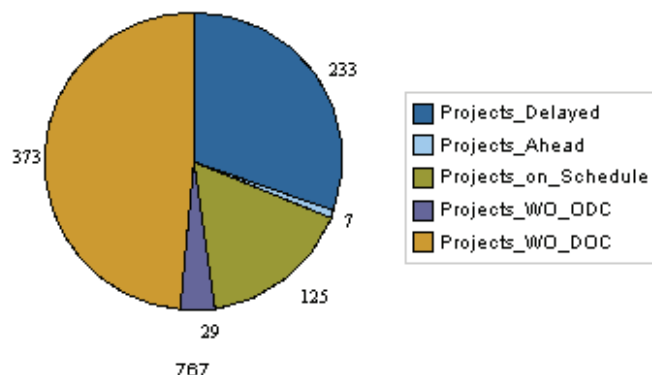

Investment Scenario

Total original cost of implementation of 767 projects when sanctioned, was of the order of Rs. 1055580.91 crore but this was subsequently revised to Rs. 1262000.07 crore implying a cost overrun of 19.6%. The expenditure incurred on these projects till July, 2015 is Rs. 499450.58 crore, which is 39.6% of the revised cost of the projects.

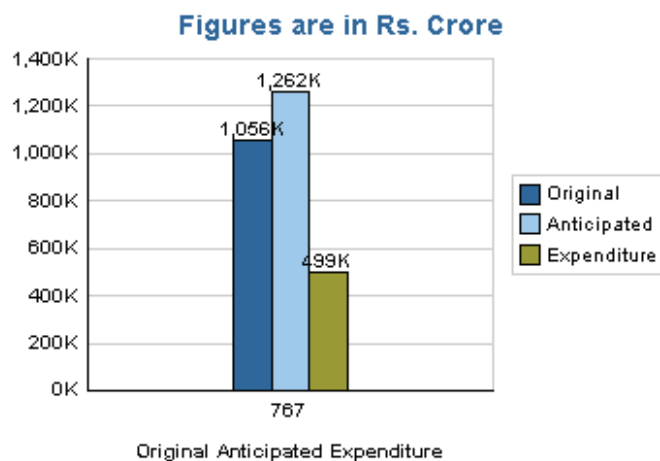

Projects Added / Completed / Dropped / Frozen

No of Projects in Previous Month	770
No of Projects Completed/Dropped/Frozen in Current Month	5
No of Projects added in Current Month	2
No of Projects in Current Month	767

Project status							
Number of Projects							
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total	Delayed Projects (%)
Original (Date)	233	7	125	29	373	767	30.38
Latest Approved (Date)	202	7	156	29	373	767	26.34

Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	652	8,55,544.82	9,41,474.74	2,95,106.62	31.30	85,929.92	10.00
Project with Revision in Cost	115	2,65,619.51	3,20,525.33	2,04,343.96	63.80	54,905.82	20.70
Total	767	11,21,164.33	12,62,000.07	4,99,450.58	39.58	140835.74	12.56
Original Cost of All Projects							
Original Cost	767	10,55,580.91	12,62,000.07	4,99,450.58	39.58	2,06,419.16	19.56

Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	233	492,382.24	601,985.63	351,503.01	58.40	109,603.39	22.30
Latest Approved	202	462,662.42	523,419.89	323,370.51	61.80	60,757.47	13.10
Total	435	955,044.66	1,125,405.52	674,873.52	59.97	170360.86	17.84

Additional Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost		Rs crore	%
20	53,687.53	56,675.29	38,984.75	68.80		2,987.76	5.60

Extent of cost overrun in projects with respect to original schedule (Sector Wise)									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost Overrun ^ (%)	No.	Original Cost	Anticipated Cost	Cost overrun ^ (%)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	2	16,663.00	22,947.00	37.71
2	CIVIL AVIATION	7	2,599.56	2,645.45	1.77	2	669.60	733.10	9.48
3	COAL	77	59,875.10	63,778.26	6.52	6	8,208.23	12,579.39	53.25
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0.00
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	0.00
6	STEEL	25	61,386.16	65,130.56	6.10	2	9,035.00	12,779.40	41.44
7	PETROCHEMICALS	1	5,460.61	9,833.52	80.08	1	5,460.61	9,833.52	80.08
8	PETROLEUM	70	142,903.11	156,858.71	9.77	17	62,721.75	78,337.61	24.90
9	POWER	109	309,271.77	349,101.15	12.88	21	55,547.32	95,440.31	71.82
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
11	RAILWAYS*	296	171,881.41	296,947.84	72.76	160	81,685.74	208,168.14	154.84
12	ROAD TRANSPORT AND HIGHWAYS	137	100,051.30	101,875.35	1.82	8	2,586.46	4,438.02	71.59
13	SHIPPING AND PORTS	6	5,539.28	5,609.32	1.26	3	1,840.06	2,502.68	36.01
14	TELECOMMUNICATIONS	2	13,718.00	13,718.00	0.00	0	0.00	0.00	0.00
15	URBAN DEVELOPMENT	30	138,680.82	143,894.82	3.76	1	6,395.00	11,609.00	81.53
Total		767	1,055,580.91	1,262,000.07	19.56	224	252,530.77	463,195.47	83.42

* - Information in respect of Ministry of Railways is as on 01.01.2015. Ministry of Railways is not updating the information.

^ - Cost Overrun = Anticipated Cost minus Original Cost.

Extent of cost overrun in projects with respect to original schedule (State Wise)									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost Overrun ^ (%)	No.	Original Cost	Anticipated Cost	Cost overrun ^ (%)
1	ANDHRA PRADESH	28	25,167.01	31,389.44	24.72	7	11,072.36	17,294.79	56.20
2	ARUNACHAL PRADESH	3	9,356.22	23,263.83	148.65	3	9,356.22	23,263.83	148.65
3	ASSAM	34	22,255.53	37,810.44	69.89	14	15,918.17	31,590.74	98.46
4	BIHAR	48	57,726.67	75,016.29	29.95	16	21,078.77	39,095.93	85.48
5	GOA	1	335.61	318.00	-5.25	0	0.00	0.00	0.00
6	GUJARAT	28	35,207.34	35,994.98	2.24	4	1,202.26	2,117.22	76.10
7	HARYANA	9	4,659.81	6,630.43	42.29	3	1,633.56	3,604.18	120.63
8	HIMACHAL PRADESH	4	7,154.09	12,973.29	81.34	2	4,966.47	10,785.67	117.17
9	JAMMU AND KASHMIR	7	21,314.62	40,235.30	88.77	2	6,142.04	25,062.72	308.05
10	KARNATAKA	34	66,982.20	81,944.97	22.34	17	13,700.79	28,669.59	109.26
11	KERALA	13	24,457.67	28,611.45	16.98	5	16,205.39	20,359.17	25.63
12	MADHYA PRADESH	20	24,954.32	26,938.24	7.95	4	2,144.95	4,548.31	112.05
13	MAHARASHTRA	47	102,713.24	113,006.17	10.02	13	21,963.17	33,300.60	51.62
14	MANIPUR	1	727.56	6,570.75	803.12	1	727.56	6,570.75	803.12
15	MEGHALAYA	3	4,845.02	6,069.90	25.28	1	4,083.02	5,307.90	30.00
16	MIZORAM	2	988.06	4,201.96	325.27	2	988.06	4,201.96	325.27
17	NAGALAND	2	5,124.00	7,461.12	45.61	2	5,124.00	7,461.12	45.61
18	ODISHA	42	72,186.50	81,274.54	12.59	15	35,919.03	45,028.41	25.36
19	PUNJAB	3	792.50	765.46	-3.41	0	0.00	0.00	0.00
20	RAJASTHAN	30	27,857.57	27,913.04	0.20	6	2,574.16	3,142.63	22.08
21	SIKKIM	2	1,648.94	4,499.46	172.87	1	1,339.48	4,190.00	212.81
22	TAMIL NADU	41	68,058.56	85,260.44	25.28	19	29,878.23	47,080.11	57.57
23	TRIPURA	6	2,966.26	6,629.97	123.51	5	2,678.22	6,376.31	138.08
24	UTTAR PRADESH	29	35,842.78	38,623.19	7.76	7	1,739.99	4,568.66	162.57
25	WEST BENGAL	38	39,963.90	49,354.81	23.50	12	4,495.64	14,409.88	220.53
26	CHANDIGARH	1	452.00	489.00	8.19	1	452.00	489.00	8.19
27	D & N HAVELI	1	6,086.08	6,086.08	0.00	0	0.00	0.00	0.00
28	DELHI	12	50,903.45	50,903.45	0.00	0	0.00	0.00	0.00
29	CHHATISGARH	28	80,681.93	82,344.10	2.06	6	3,494.57	5,157.04	47.57
30	JHARKHAND	37	38,977.33	39,535.41	1.43	5	1,172.18	1,772.00	51.17
31	UTTARAKHAND	6	9,351.89	12,905.21	38.00	4	7,346.89	10,900.21	48.37
32	ANDAMAN & NICOBAR ISLANDS	1	314.61	314.61	0.00	0	0.00	0.00	0.00
33	TELANGANA	22	9,807.71	12,632.35	28.80	6	1,903.46	4,728.10	148.40
34	MULTI STATE	184	195,719.93	224,032.39	14.47	41	23,230.13	52,118.64	124.36
Total		767	1,055,580.91	1,262,000.07	19.56	224	252,530.77	463,195.47	83.42

^ - Cost Overrun = Anticipated Cost minus Original Cost.

Extent of time overrun in projects with respect to original schedule									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns \$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost Overrun ^ (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	4	40,442.00	46,726.00	17 - 82
2	CIVIL AVIATION	7	2,599.56	2,645.45	1.77	3	979.06	1,042.56	4 - 80
3	COAL	77	59,875.10	63,778.26	6.52	44	31,159.10	35,167.24	8 - 84
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	-
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	-
6	STEEL	25	61,386.16	65,130.56	6.10	12	43,203.04	43,203.04	6 - 44
7	PETROCHEMICALS	1	5,460.61	9,833.52	80.08	1	5,460.61	9,833.52	41 - 41
8	PETROLEUM	70	142,903.11	156,858.71	9.77	42	95,729.95	103,011.27	3 - 71
9	POWER	109	309,271.77	349,101.15	12.88	59	144,523.04	171,759.47	5 - 123
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
11	RAILWAYS*	296	171,881.41	296,947.84	72.76	31	31,140.62	88,821.64	3 - 261
12	ROAD TRANSPORT AND HIGHWAYS	137	100,051.30	101,875.35	1.82	21	15,568.71	15,832.41	6 - 94
13	SHIPPING AND PORTS	6	5,539.28	5,609.32	1.26	1	366.39	669.46	61 - 61
14	TELECOMMUNICATIONS	2	13,718.00	13,718.00	0.00	1	384.00	384.00	59 - 59
15	URBAN DEVELOPMENT	30	138,680.82	143,894.82	3.76	13	81,707.72	81,707.72	2 - 34
Total		767	1,055,580.91	1,262,000.07	19.56	233	492,382.24	601,985.63	

* - Information in respect of Ministry of Railways is as on 01.01.2015. Ministry of Railways is not updating the information.

\$ - Time Overrun = Anticipated Date of Commissioning minus Original Date of Commissioning.

^ - Cost Overrun = Anticipated Cost minus Original Cost.

Extent of time overrun in projects with respect to original schedule (State Wise)									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns \$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost Overrun ^ (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	28	25,167.01	31,389.44	24.72	3	1,958.89	1,958.89	8 - 22
2	ARUNACHAL PRADESH	3	9,356.22	23,263.83	148.65	2	3,070.89	7,963.83	31 - 87
3	ASSAM	34	22,255.53	37,810.44	69.89	15	18,161.44	32,790.99	15 - 110
4	BIHAR	48	57,726.67	75,016.29	29.95	7	20,548.45	31,923.97	5 - 98
5	GOA	1	335.61	318.00	-5.25	0	0.00	0.00	-
6	GUJARAT	28	35,207.34	35,994.98	2.24	6	20,257.81	20,181.12	19 - 48
7	HARYANA	9	4,659.81	6,630.43	42.29	0	0.00	0.00	-
8	HIMACHAL PRADESH	4	7,154.09	12,973.29	81.34	2	4,190.42	8,089.51	11 - 111
9	JAMMU AND KASHMIR	7	21,314.62	40,235.30	88.77	2	6,142.04	25,062.72	10 - 193
10	KARNATAKA	34	66,982.20	81,944.97	22.34	5	3,785.71	4,845.36	12 - 96
11	KERALA	13	24,457.67	28,611.45	16.98	2	1,600.06	2,300.06	15 - 48
12	MADHYA PRADESH	20	24,954.32	26,938.24	7.95	6	2,304.29	2,206.15	12 - 69
13	MAHARASHTRA	47	102,713.24	113,006.17	10.02	18	59,647.88	65,823.55	2 - 144
14	MANIPUR	1	727.56	6,570.75	803.12	1	727.56	6,570.75	96 - 96
15	MEGHALAYA	3	4,845.02	6,069.90	25.28	0	0.00	0.00	-
16	MIZORAM	2	988.06	4,201.96	325.27	2	988.06	4,201.96	47 - 123
17	NAGALAND	2	5,124.00	7,461.12	45.61	1	850.00	2,973.42	60 - 60
18	ODISHA	42	72,186.50	81,274.54	12.59	18	40,948.91	46,120.60	6 - 84
19	PUNJAB	3	792.50	765.46	-3.41	0	0.00	0.00	-
20	RAJASTHAN	30	27,857.57	27,913.04	0.20	3	15,814.00	15,386.02	17 - 39
21	SIKKIM	2	1,648.94	4,499.46	172.87	2	1,648.94	4,499.46	51 - 80
22	TAMIL NADU	41	68,058.56	85,260.44	25.28	11	51,578.96	61,493.93	8 - 90
23	TRIPURA	6	2,966.26	6,629.97	123.51	3	2,129.35	5,125.93	25 - 108
24	UTTAR PRADESH	29	35,842.78	38,623.19	7.76	7	11,507.29	12,974.60	9 - 84
25	WEST BENGAL	38	39,963.90	49,354.81	23.50	11	17,184.44	21,446.19	3 - 177
26	CHANDIGARH	1	452.00	489.00	8.19	1	452.00	489.00	4 - 4
27	D & N HAVELI	1	6,086.08	6,086.08	0.00	1	6,086.08	6,086.08	10 - 10
28	DELHI	12	50,903.45	50,903.45	0.00	5	42,630.16	42,630.16	9 - 34
29	CHHATISGARH	28	80,681.93	82,344.10	2.06	14	55,685.34	56,167.40	12 - 72
30	JHARKHAND	37	38,977.33	39,535.41	1.43	19	12,461.36	12,875.85	2 - 138
31	UTTARAKHAND	6	9,351.89	12,905.21	38.00	3	7,127.06	10,570.24	69 - 94
32	ANDAMAN & NICOBAR ISLANDS	1	314.61	314.61	0.00	0	0.00	0.00	-
33	TELANGANA	22	9,807.71	12,632.35	28.80	11	3,359.39	4,375.44	8 - 72
34	MULTI STATE	184	195,719.93	224,032.39	14.47	52	79,535.46	84,852.45	4 - 261
Total		767	1,055,580.91	1,262,000.07	19.56	233	492,382.24	601,985.63	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus Original Cost.

Extent of time overrun in projects with respect to latest schedule									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns \$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost Overrun ^ (%)	No.	Original cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	3	36,950.00	41,049.00	17 - 82
2	CIVIL AVIATION	7	2,599.56	2,645.45	1.77	3	979.06	1,042.56	4 - 80
3	COAL	77	59,875.10	63,778.26	6.52	42	24,021.72	28,029.86	8 - 84
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	-
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	-
6	STEEL	25	61,386.16	65,130.56	6.10	11	27,678.04	27,678.04	6 - 44
7	PETROCHEMICALS	1	5,460.61	9,833.52	80.08	1	5,460.61	9,833.52	41 - 41
8	PETROLEUM	70	142,903.11	156,858.71	9.77	26	67,932.53	73,306.93	3 - 71
9	POWER	109	309,271.77	349,101.15	12.88	58	142,026.14	165,283.13	5 - 123
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
11	RAILWAYS *	296	171,881.41	296,947.84	72.76	28	24,665.62	76,297.64	3 - 261
12	ROAD TRANSPORT AND HIGHWAYS	137	100,051.30	101,875.35	1.82	14	14,138.98	14,310.73	6 - 85
13	SHIPPING AND PORTS	6	5,539.28	5,609.32	1.26	1	366.39	669.46	61 - 61
14	TELECOMMUNICATIONS	2	13,718.00	13,718.00	0.00	1	384.00	384.00	59 - 59
15	URBAN DEVELOPMENT	30	138,680.82	143,894.82	3.76	13	81,707.72	81,707.72	2 - 34
Total		767	1,055,580.91	1,262,000.07	19.56	202	428,028.81	523,419.89	

* - Information in respect of Ministry of Railways is as on 01.01.2015. Ministry of Railways is not updating the information.

\$ - Time Overrun = Anticipated Date of Commissioning minus Original Date of Commissioning.

^ - Cost Overrun = Anticipated Cost minus Original Cost.

Extent of cost overrun in projects with respect to latest schedule									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overruns ^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun ^ (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun ^ (%)
1	ATOMIC ENERGY	4	46,726.00	46,726.00	0.00	0	0.00	0.00	0.00
2	CIVIL AVIATION	7	2,636.56	2,645.45	0.34	1	217.60	244.10	12.18
3	COAL	77	63,938.96	63,778.26	-0.25	2	630.12	678.22	7.63
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0.00
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	0.00
6	STEEL	25	64,985.16	65,130.56	0.22	1	343.00	488.40	42.39
7	PETROCHEMICALS	1	8,920.00	9,833.52	10.24	1	8,920.00	9,833.52	10.24
8	PETROLEUM	70	154,272.56	156,858.71	1.68	6	16,219.52	19,055.34	17.48
9	POWER	109	332,210.44	349,101.15	5.08	5	17,399.92	34,290.63	97.07
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
11	RAILWAYS*	296	185,296.44	296,947.84	60.26	154	87,045.00	200,328.20	130.14
12	ROAD TRANSPORT AND HIGHWAYS	137	100,165.25	101,875.35	1.71	7	2,368.85	4,128.46	74.28
13	SHIPPING AND PORTS	6	5,842.35	5,609.32	-3.99	2	1,473.67	1,833.22	24.40
14	TELECOMMUNICATIONS	2	13,718.00	13,718.00	0.00	0	0.00	0.00	0.00
15	URBAN DEVELOPMENT	30	138,680.82	143,894.82	3.76	1	6,395.00	11,609.00	81.53
Total		767	1,121,164.33	1,262,000.07	12.56	181	142,730.68	286,316.39	100.60

* - Information in respect of Ministry of Railways is as on 01.01.2015. Ministry of Railways is not updating the information.

\$ - Time Overrun = Anticipated Date of Commissioning minus Original Date of Commissioning.

^ - Cost Overrun = Anticipated Cost minus Latest Approved Cost..

Extent of time & cost overrun in projects with respect to latest schedule									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	1	3,492.00	5,677.00	72- 72
2	CIVIL AVIATION	7	2,599.56	2,645.45	1.77	0	0.00	0.00	0- 0
3	COAL	77	59,875.10	63,778.26	6.52	2	6,935.32	10,186.51	41- 73
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0- 0
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	0- 0
6	STEEL	25	61,386.16	65,130.56	6.10	1	8,692.00	12,291.00	66- 66
7	PETROCHEMICALS	1	5,460.61	9,833.52	80.08	1	5,460.61	9,833.52	41- 41
8	PETROLEUM	70	142,903.11	156,858.71	9.77	7	37,617.12	48,353.39	12- 110
9	POWER	109	309,271.77	349,101.15	12.88	10	22,160.66	36,842.84	16- 123
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	0	0.00	0.00	0- 0
11	RAILWAYS*	296	171,881.41	296,947.84	72.76	4	5,873.07	10,121.84	48- 174
12	ROAD TRANSPORT AND HIGHWAYS	137	100,051.30	101,875.35	1.82	2	425.61	517.56	69- 93
13	SHIPPING AND PORTS	6	5,539.28	5,609.32	1.26	0	0.00	0.00	0- 0
14	TELECOMMUNICATIONS	2	13,718.00	13,718.00	0.00	0	0.00	0.00	0- 0
15	URBAN DEVELOPMENT	30	138,680.82	143,894.82	3.76	0	0.00	0.00	0- 0
Total		767	1055580.91	1262000.07	19.56	28	90656.39	133823.66	

* - Information in respect of Ministry of Railways is as on 01.01.2015. Ministry of Railways is not updating the information.

\$ - Time Overrun = Anticipated Date of Commissioning minus Original Date of Commissioning.

^ - Cost Overrun = Anticipated Cost minus Original Cost.

<u>Extent of time & cost overrun in projects with respect to original schedule</u>									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	2	16,663.00	22,947.00	72- 82
2	CIVIL AVIATION	7	2,599.56	2,645.45	1.77	2	669.60	733.10	4- 6
3	COAL	77	59,875.10	63,778.26	6.52	4	7,627.19	11,894.53	36- 73
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0- 0
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	0- 0
6	STEEL	25	61,386.16	65,130.56	6.10	0	0.00	0.00	0- 0
7	PETROCHEMICALS	1	5,460.61	9,833.52	80.08	1	5,460.61	9,833.52	41- 41
8	PETROLEUM	70	142,903.11	156,858.71	9.77	10	39,983.40	48,757.91	12- 51
9	POWER	109	309,271.77	349,101.15	12.88	18	41,624.08	68,924.12	10- 123
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75- 75
11	RAILWAYS*	296	171,881.41	296,947.84	72.76	27	22,946.70	80,627.72	3- 261
12	ROAD TRANSPORT AND HIGHWAYS	137	100,051.30	101,875.35	1.82	3	527.65	791.35	69- 85
13	SHIPPING AND PORTS	6	5,539.28	5,609.32	1.26	1	366.39	669.46	61- 61
14	TELECOMMUNICATIONS	2	13,718.00	13,718.00	0.00	0	0.00	0.00	0- 0
15	URBAN DEVELOPMENT	30	138,680.82	143,894.82	3.76	0	0.00	0.00	0- 0
Total		767	1055580.91	1262000.07	19.56	69	137586.62	249006.01	

* - Information in respect of Ministry of Railways is as on 01.01.2015. Ministry of Railways is not updating the information.

\$ - Time Overrun = Anticipated Date of Commissioning minus Original Date of Commissioning.

^ - Cost Overrun = Anticipated Cost minus Original Cost.

List of projects completed/dropped/Frozen during current month							(All Cost /Expenditure in Rs. crore)
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>PETROLEUM</u>						
1	SURAT PARADIP PIPELINE PROJECT	10/2012	10,281.00	04/2015	10,281.00	N.A.	1.49
	<u>POWER</u>						
2	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID	06/2012	1,263.26	11/2014	1,263.26	07/2015	1,131.58
	<u>SHIPPING AND PORTS</u>						
3	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	03/2006	600.00	07/2015	139.80
4	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS	02/2011	830.00	05/2013	621.53	07/2015	.01
	<u>STEEL</u>						
5	AUGMENTATION OF IRON ORE STORAGE IN RMHP	07/2007	480.00	09/2009	450.00	07/2015	388.52

List of projects added					(All Cost in Rs. crore)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>COAL</u>					
1	KAKATIYAKHANI OPENCAST-2 PROJECT	5/2015	397.09	3/2019	397.09	3/2019
	<u>SHIPPING AND PORTS</u>					
2	ACQUISITION OF TWO (2) NOS OF 317000 DWT VLCC'S FROM JIANGSU RONGSHENG HEAVY INDUSTRIES CO.LTD.,CHIN	10/2010	994.82	11/2013	402.24	11/2013


Milestones (Cumulative due & achieved)

Total	3774
Achieved up to month	1725


List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>CIVIL AVIATION</u>						
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT AAI	309.46	309.46	01/2011	06/2017	09/2017	3
	<u>COAL</u>						
2	TUTICORIN THERMAL POWER PROJECT- 2X500 MW NLC	4,904.54	6,602.74	03/2012	07/2015	08/2015	1
3	ADRIYALA SHAFT PROJECT SCCL	212.34	1,228.39	03/2013	09/2015	03/2016	6
4	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI NCL	259.40	259.40	03/2012	03/2016	03/2017	12
	<u>STEEL</u>						
5	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP SAIL	160.48	160.48	09/2014	06/2015	07/2015	1
	<u>PETROLEUM</u>						
6	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II ONGC	5,608.40	5,608.40	05/2015	07/2015	08/2015	1
7	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY IOCL	480.00	480.00	02/2016	05/2016	07/2016	2
8	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS ONGC	4,124.35	4,124.35	04/2016	04/2017	12/2017	8
	<u>POWER</u>						
9	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. PGCIL	4,672.99	4,672.99	11/2012	07/2015	08/2015	1
10	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A PGCIL	2,074.86	2,348.37	03/2013	09/2015	10/2015	1
11	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) PGCIL	213.78	213.78	03/2014	07/2015	08/2015	1

List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
12	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH PGCIL	1,961.87	1,961.87	05/2014	03/2016	06/2016	3
13	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH PGCIL	9,569.76	9,569.76	06/2015	03/2016	06/2016	3
14	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B PGCIL	2,514.88	2,514.88	12/2015	03/2016	06/2016	3
15	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I PGCIL	374.63	374.63	04/2016	04/2016	11/2016	7
16	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C PGCIL	514.20	514.20	06/2015	12/2015	08/2016	8
17	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI PGCIL	1,909.24	1,909.24	06/2015	12/2015	08/2016	8
18	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT PGCIL	11,130.19	11,130.19	08/2013	03/2016	12/2016	9
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
19	GUWAHATI TO NALBARI (AS-5) NHAI	198.16	198.16	04/2008	08/2015	12/2015	4
	<u>URBAN DEVELOPMENT</u>						
20	FARIDABAD EXTENSION DMRCL	2,494.00	2,494.00	09/2014	05/2015	08/2015	3

Graphical Presentation of All Projects w.r.t. Original Schedule

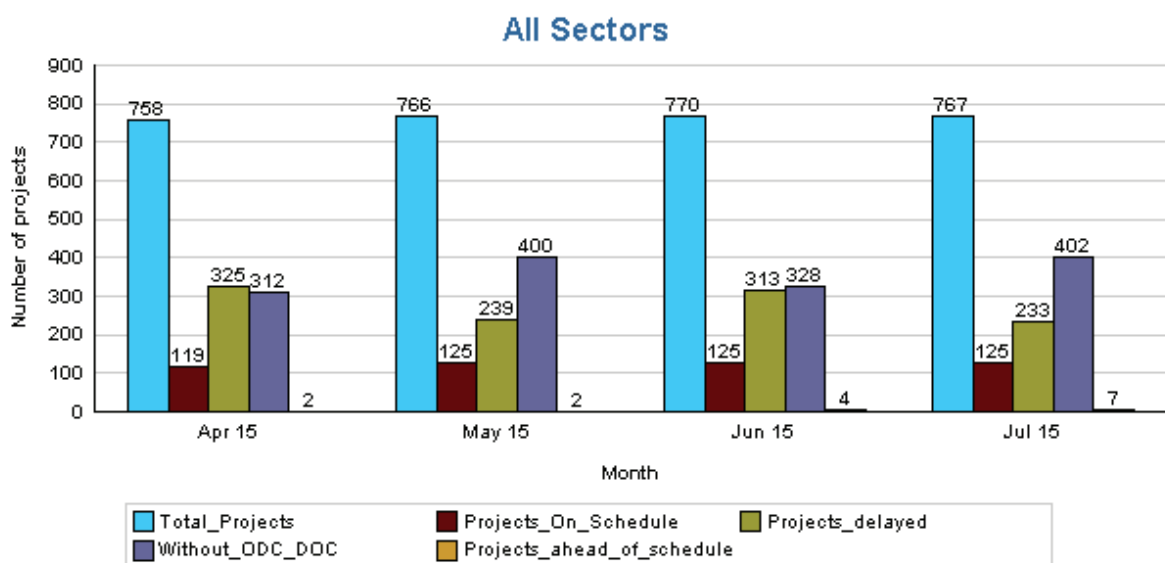


Break-up of 233 Delayed projects in July 2015

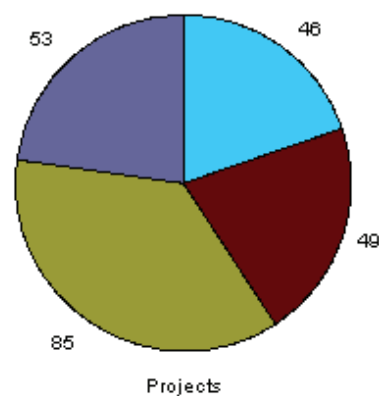


Delay in Months: 1-12 (Light Blue), 13-24 (Dark Red), 25-60 (Olive Green), MORE THAN 60 (Purple)


Graphical Presentation of ATOMIC ENERGY Sector

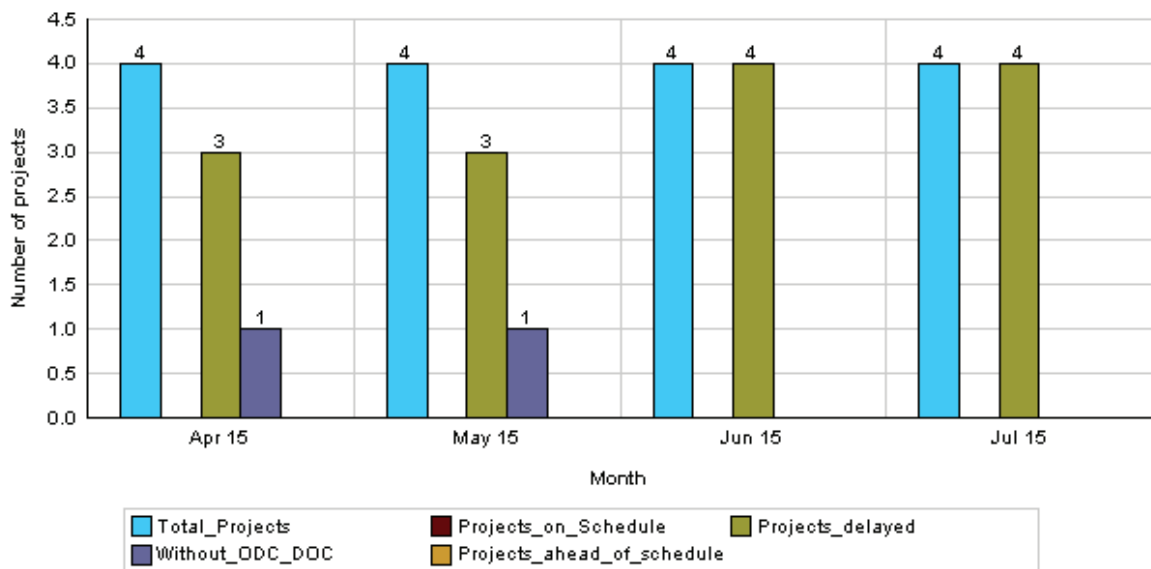


Break-up of 4 Delayed projects in July 2015

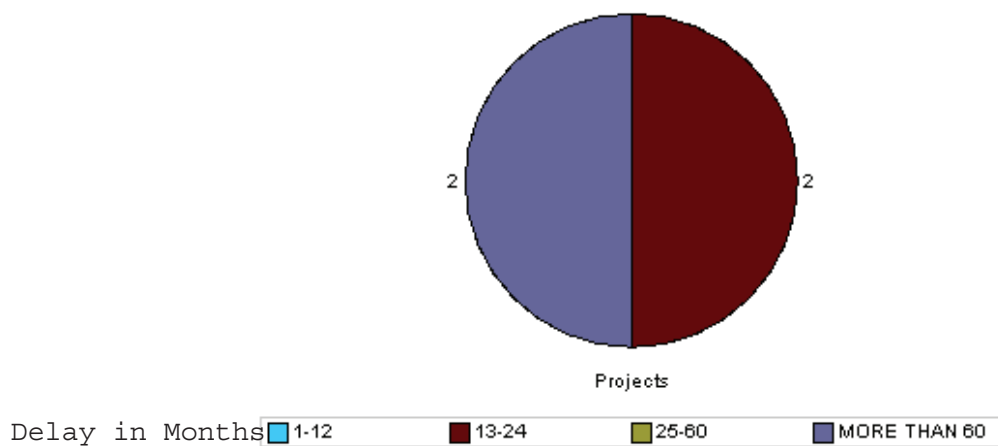

Graphical Presentation of CIVIL AVIATION Sector

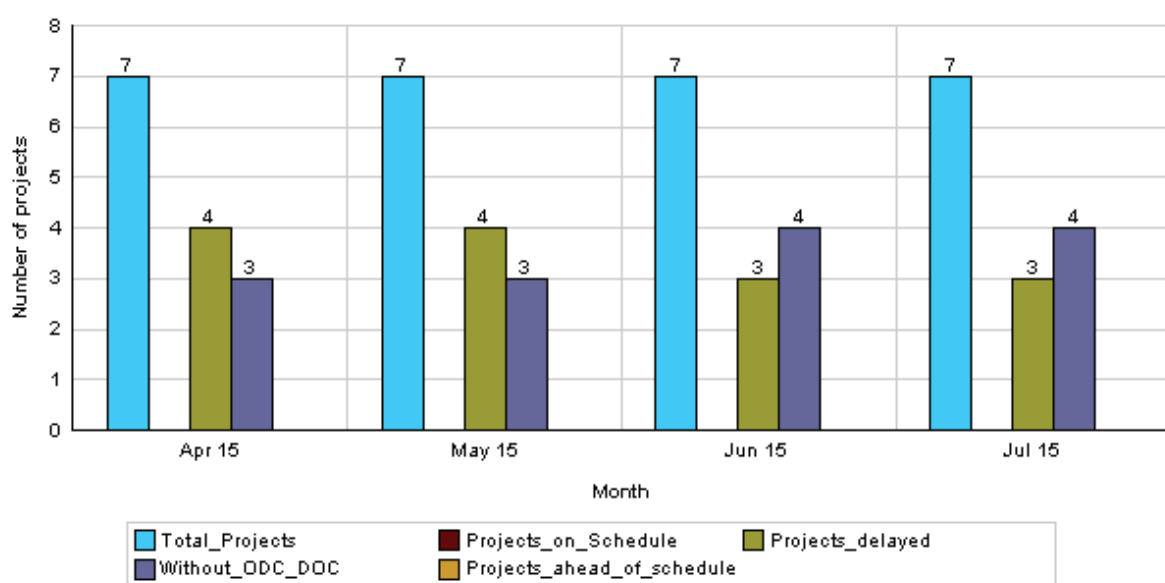


Break-up of 3 Delayed projects in July 2015

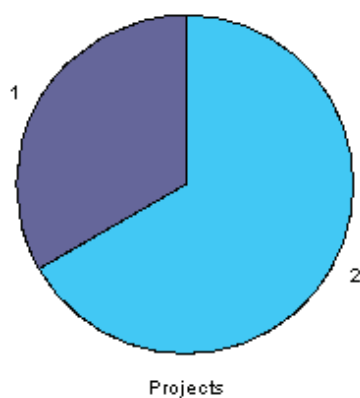


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60


Graphical Presentation of COAL Sector

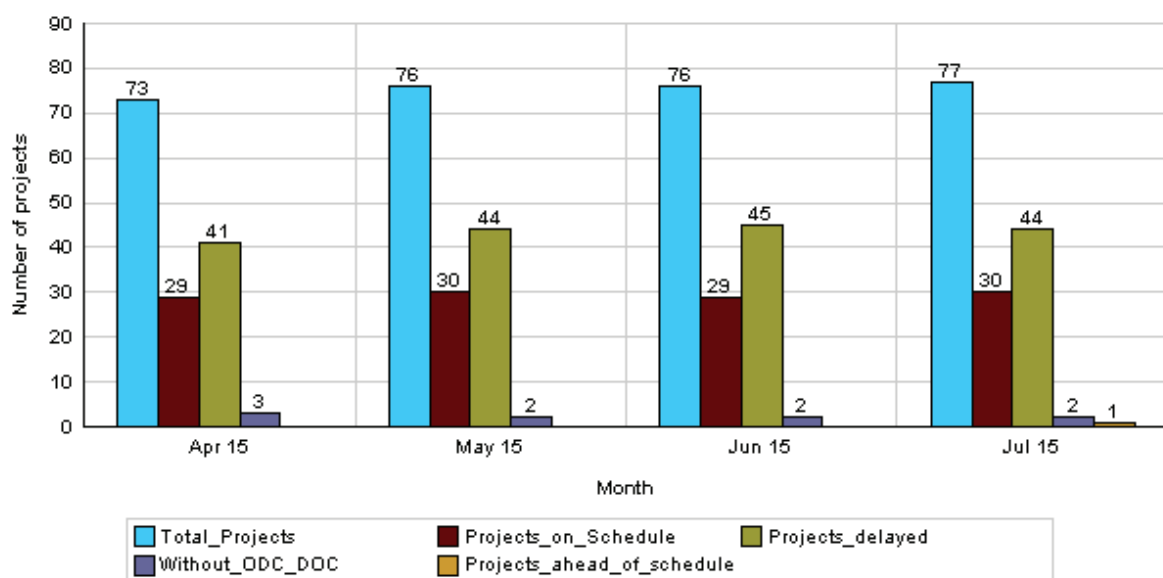

Break-up of 44 Delayed projects in July 2015

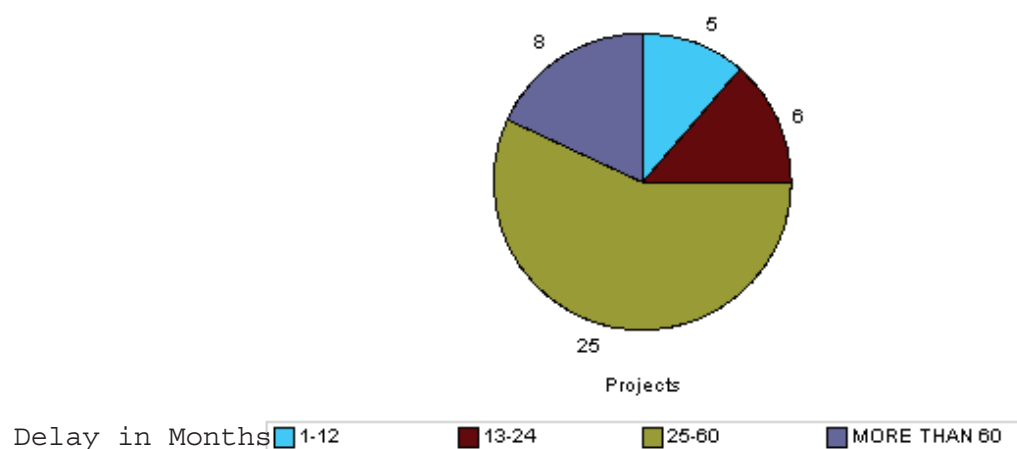

Graphical Presentation of STEEL Sector

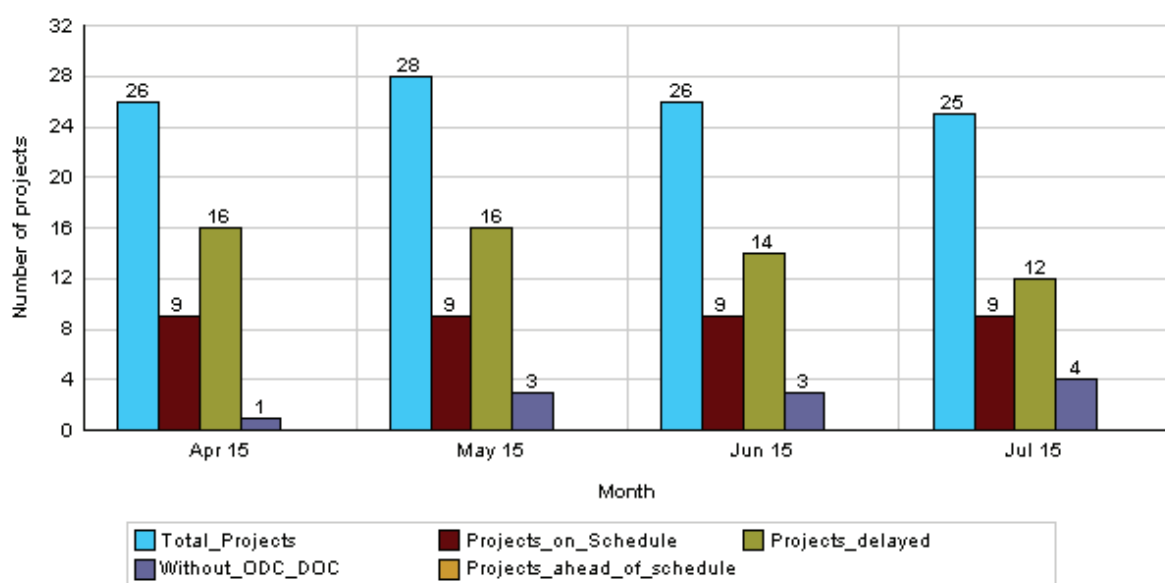


Break-up of 12 Delayed projects in July 2015




Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of PETROLEUM Sector

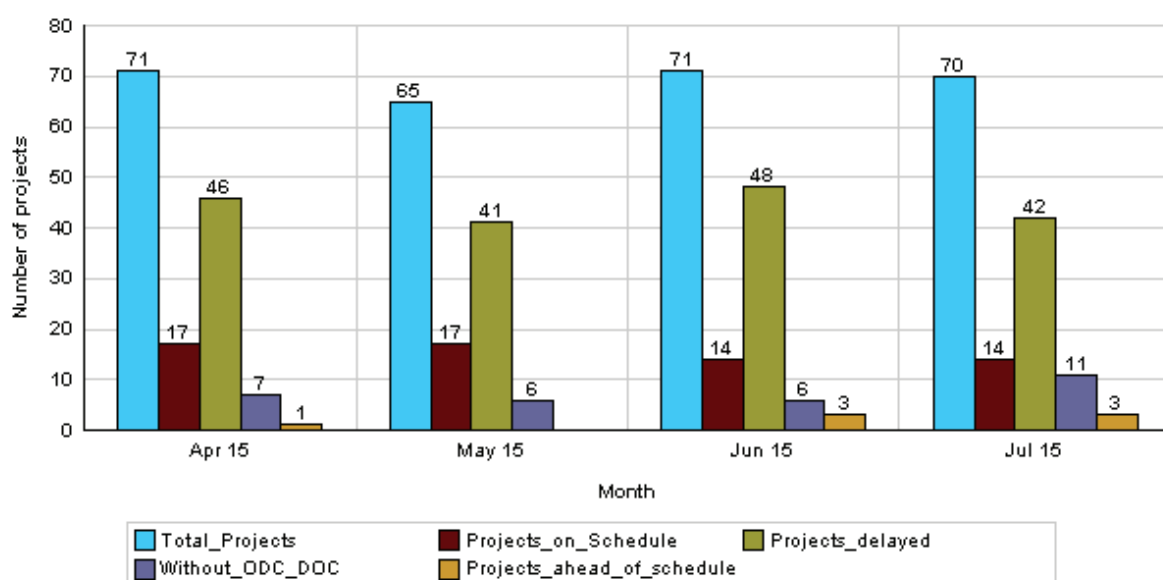


Break-up of 42 Delayed projects in July 2015

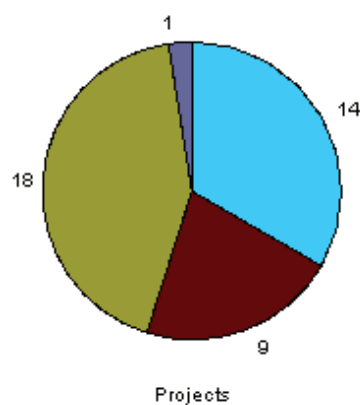


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60


Graphical Presentation of POWER Sector

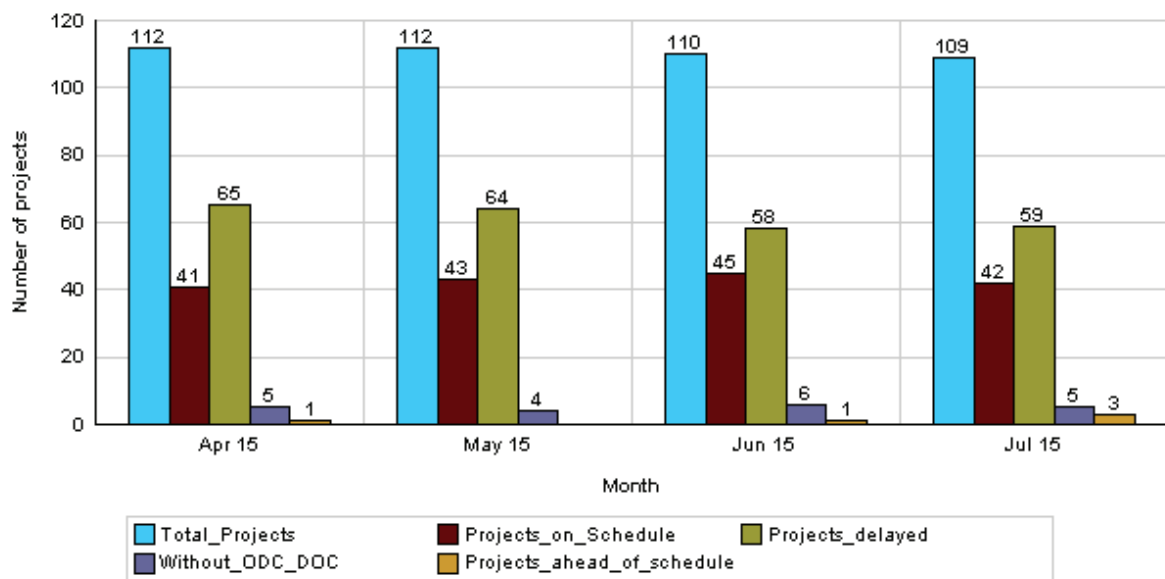


Break-up of 59 Delayed projects in July 2015

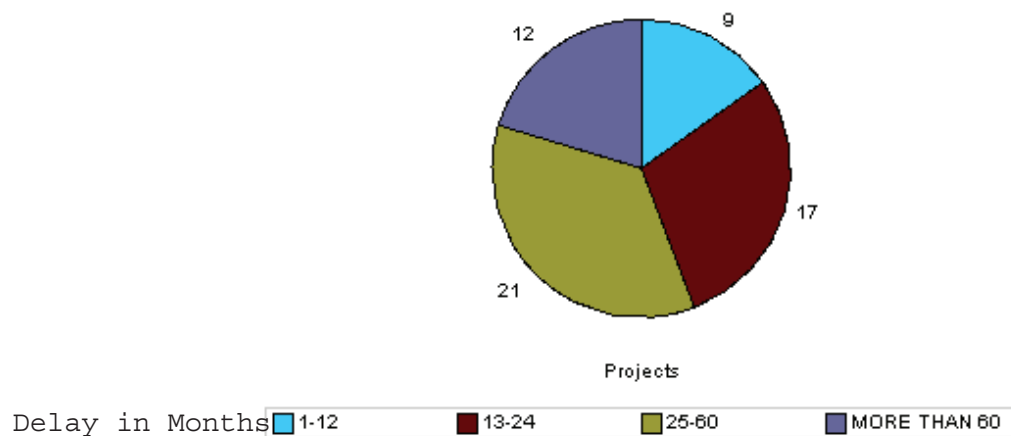

Graphical Presentation of RAILWAYS Sector

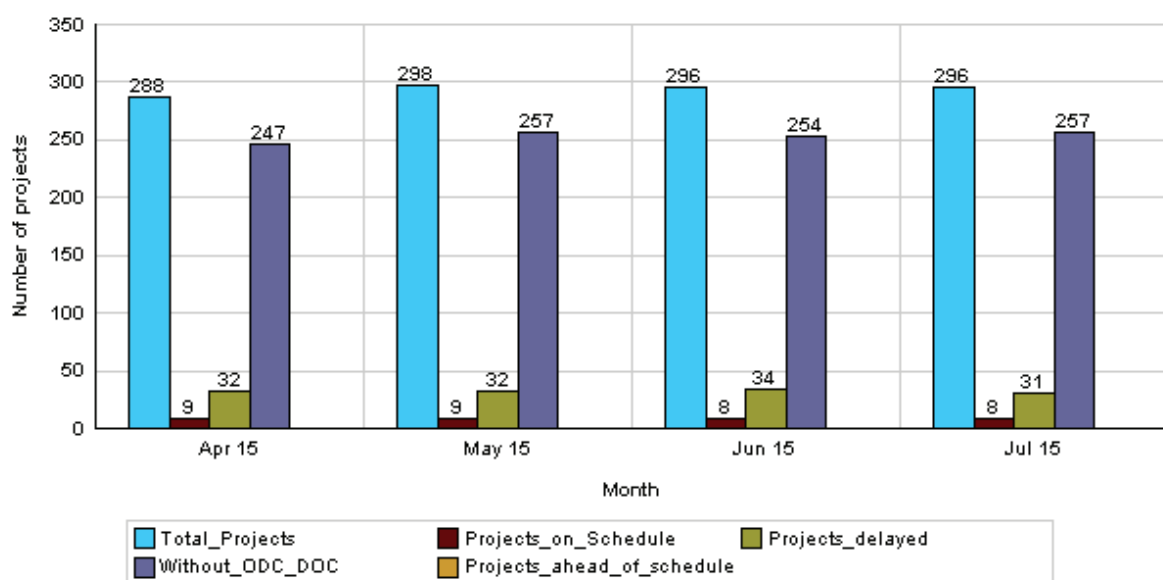


Break-up of 31 Delayed projects in July 2015

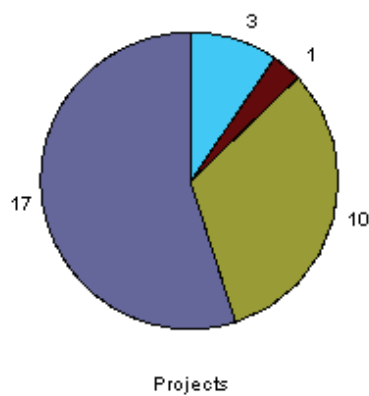


Delay in Months: 1-12, 13-24, 25-60, MORE THAN 60

Graphical Presentation of ROAD TRANSPORT AND HIGHWAYS Sector

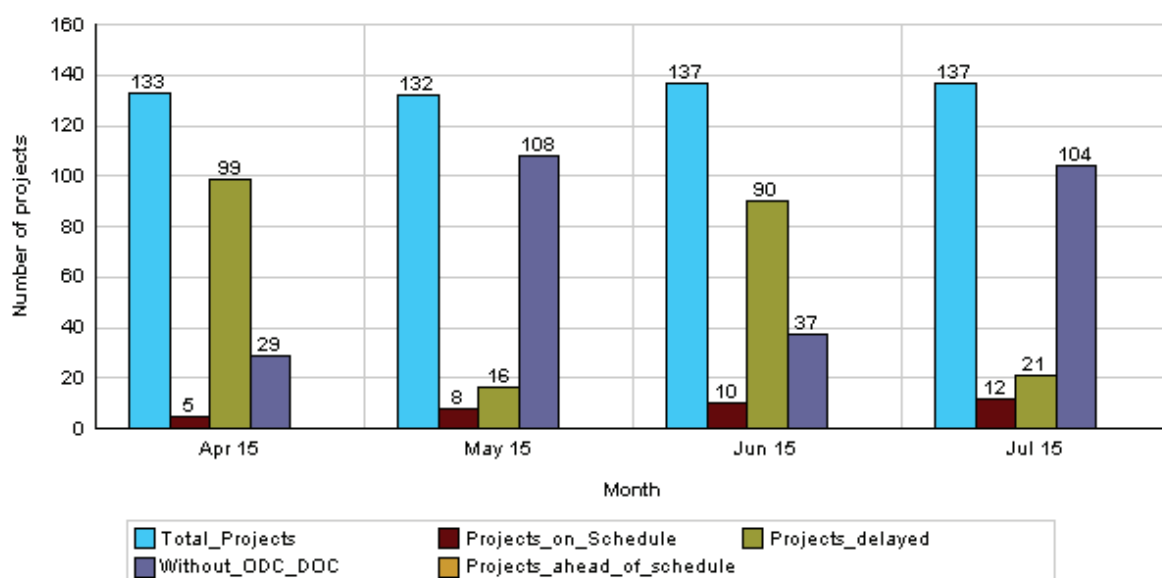


Break-up of 21 Delayed projects in July 2015

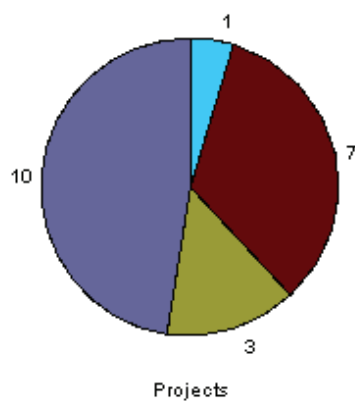


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60


Graphical Presentation of SHIPPING AND PORTS Sector

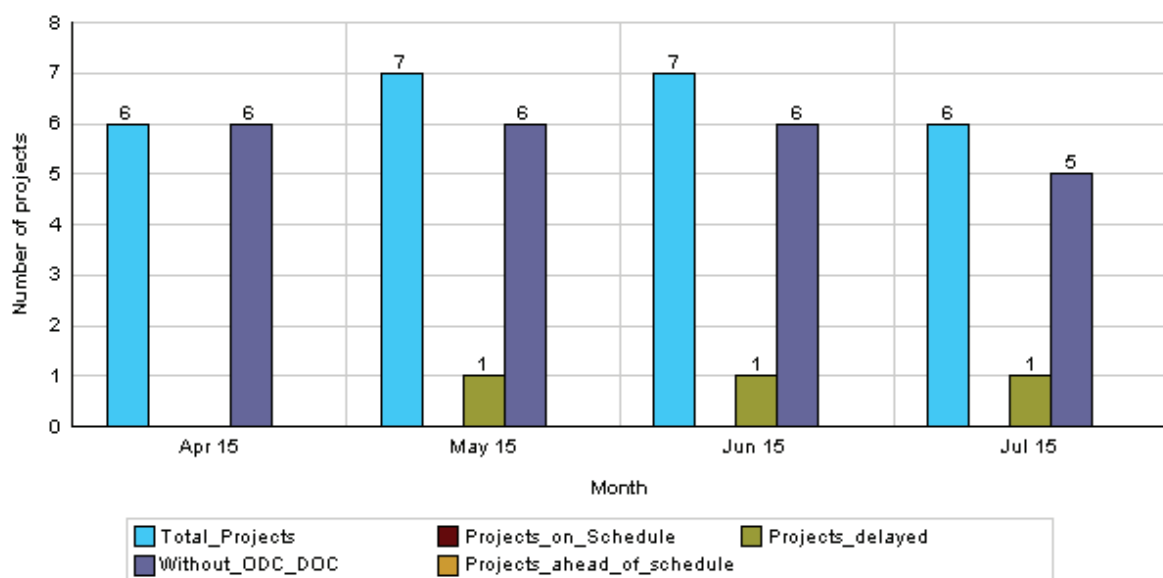


Break-up of 1 Delayed projects in July 2015

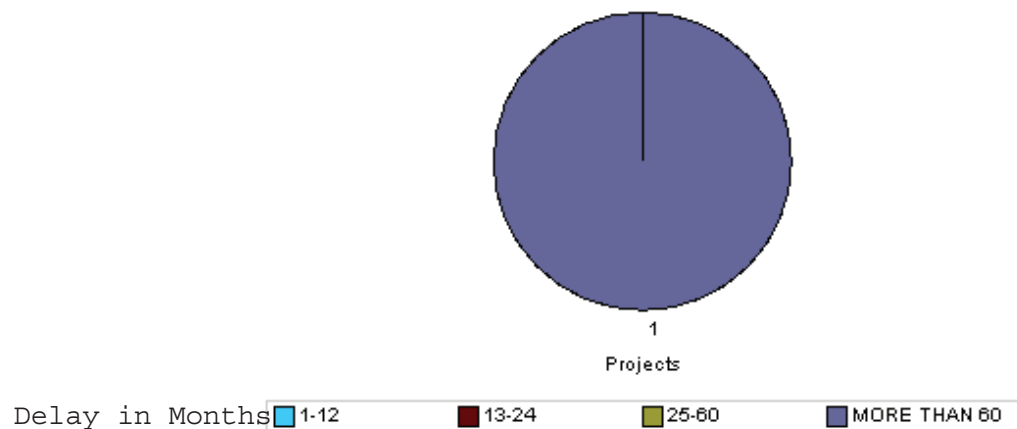


Graphical Presentation of TELECOMMUNICATIONS Sector

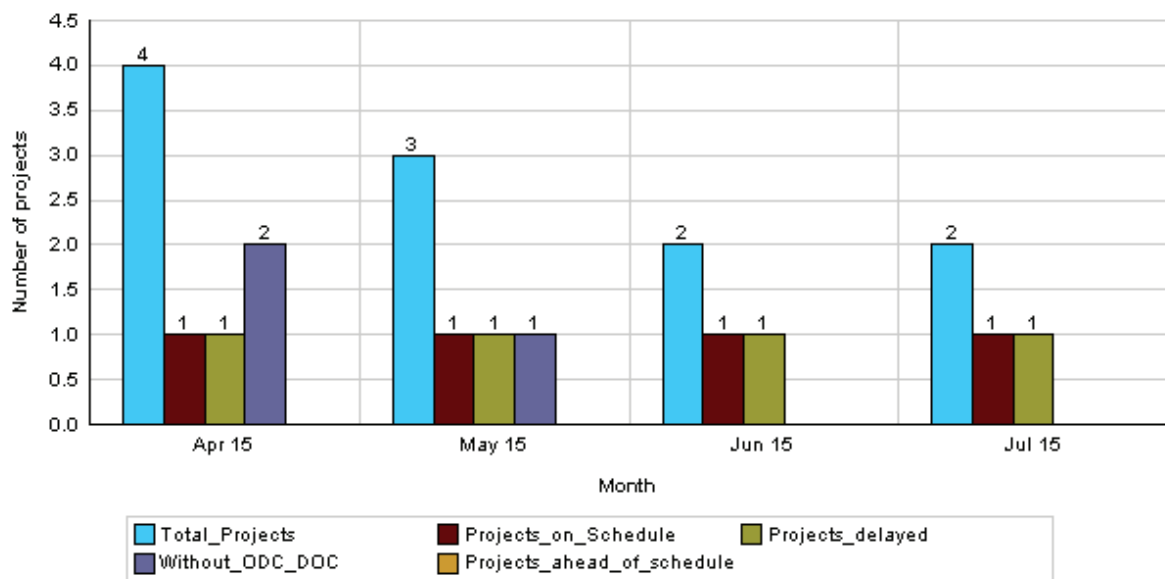


Break-up of 1 Delayed projects in July 2015

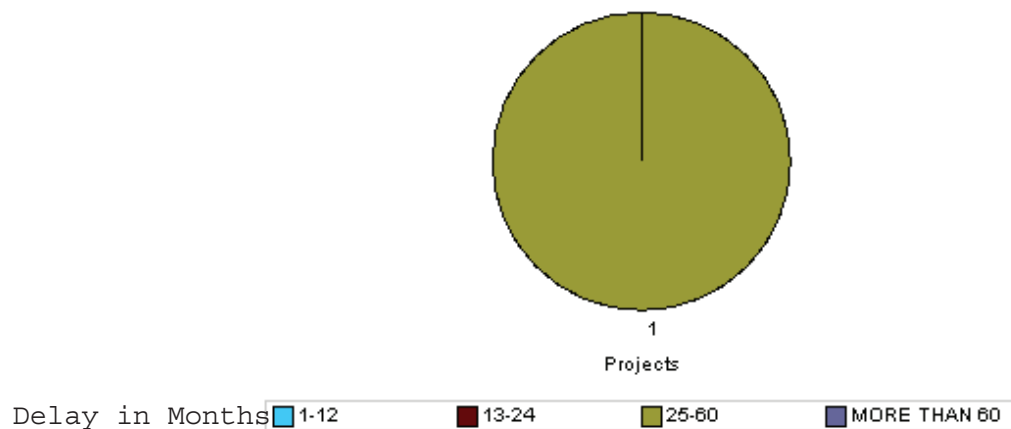

Graphical Presentation of URBAN DEVELOPMENT Sector

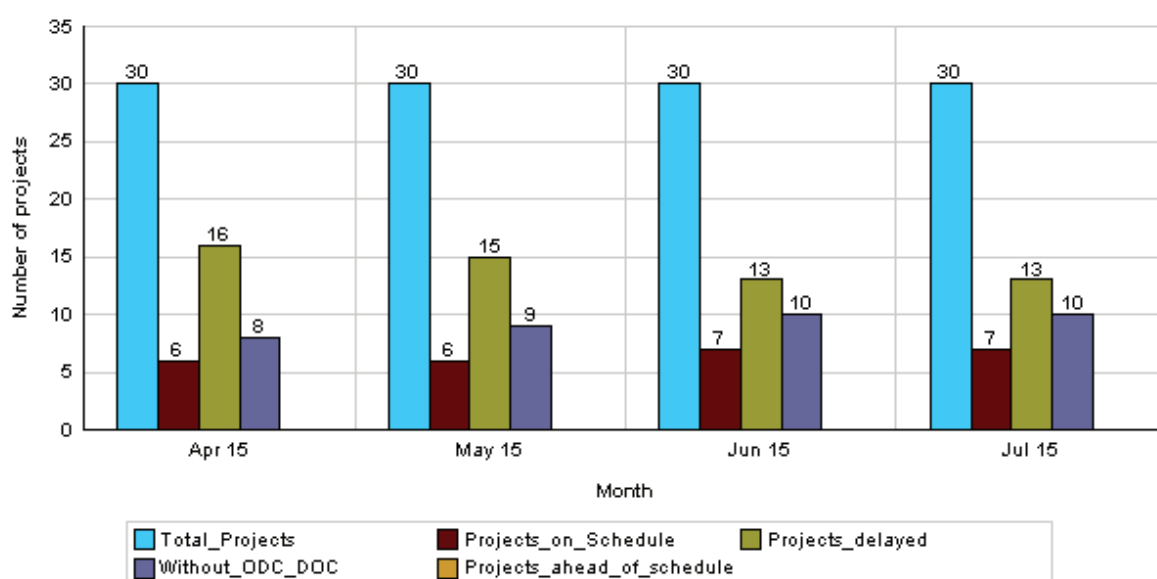

Break-up of 13 Delayed projects in July 2015

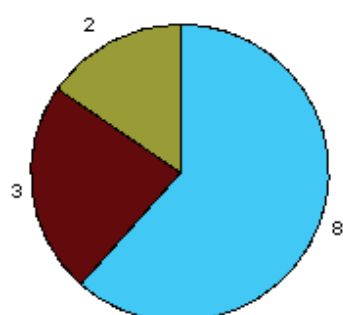

Delay in Months: 1-12, 13-24, 25-60, MORE THAN 60

Sectorwise analysis of projects					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	40,442.00	46,726.00	46,726.00	37,266.21
CIVIL AVIATION	7	2,599.56	2,636.56	2,645.45	1,698.08
COAL	77	59,875.10	63,938.96	63,778.26	22,605.99
FERTILISERS	1	197.79	197.79	197.79	24.66
MINES	1	1,856.00	1,856.00	1,856.00	0.00
STEEL	25	61,386.16	64,985.16	65,130.56	42,250.74
PETROCHEMICALS	1	5,460.61	8,920.00	9,833.52	8,784.45
PETROLEUM	70	142,903.11	154,272.56	156,858.71	72,984.98
POWER	109	309,271.77	332,210.44	349,101.15	172,846.68
HEAVY INDUSTRY	1	1,718.00	1,718.00	3,827.30	0.00
RAILWAYS	296	171,881.41	185,296.44	296,947.84	87,417.33
ROAD TRANSPORT AND HIGHWAYS	137	100,051.30	100,165.25	101,875.35	19,064.80
SHIPPING AND PORTS	6	5,539.28	5,842.35	5,609.32	3,066.85
TELECOMMUNICATIONS	2	13,718.00	13,718.00	13,718.00	66.02
URBAN DEVELOPMENT	30	138,680.82	138,680.82	143,894.82	31,373.79
Grand total	767	1,055,580.91	1,121,164.33	1,262,000.07	499,450.58

(All Cost/ Expenditure in Rs. Crore)

Sector Wise Details									
(July 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00	11,459.00	6,853.00	12/2015	10/2017	22(O)	4/70
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL, TAMIL NADU	12/2001	13,171.00	17,270.00	20,713.00	12/2008	10/2015	82(O)	40/102
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI, TAMIL NADU	09/2003	3,492.00	5,677.00	5,031.21	09/2010	09/2016	72(O)	12/88
4	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00	12,320.00	4,669.00	12/2016	05/2018	17(O)	4/69
	Total		40,442.00	46,726.00	37,266.21				60/329
	<u>CIVIL AVIATION</u>								
5	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI, SIKKIM	01/2009	309.46	309.46	357.35	01/2011	09/2017	80(O)	0/0
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, ANDAMAN & NICOBAR ISLANDS	10/2013	314.61	314.61	17.82	-	09/2018	-	0/0
7	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI, GOA	05/2010	335.61	318.00	301.94	05/2012	03/2015	-	0/0
8	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]AAI, CHANDIGARH	02/2011	452.00	489.00	468.24	03/2015	07/2015	4(O)	0/0
9	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI, MULTI STATE	02/2010	344.28	344.28	69.16	03/2014	05/2015	-	0/0
10	GAGAN PROJECT - [N04000065]AAI, MULTI STATE	09/2008	626.00	626.00	483.53	06/2013	-	-	0/0
11	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI, MULTI STATE	10/2012	217.60	244.10	0.04	03/2015	09/2015	6(O)	0/0
	Total		2,599.56	2,645.45	1,698.08				0/0
	<u>COAL</u>								
12	ADRIYALA SHAFT PROJECT - [N06000016]SCCL, TELANGANA	12/2009	212.34	1,228.39	859.79	03/2013	03/2016	36(O)	21/22
13	AMERA OC RCE - [N06000123]SECL, CHHATISGARH	02/2015	335.97	335.97	29.73	03/2018	03/2018	0(O)	0/4
14	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL, CHHATISGARH	11/2009	150.59	198.59	111.96	03/2016	03/2016	0(O)	3/7
15	AMLOHRI EPR (NCL) (6 MTY, INCR.) - [N06000010]NCL, MADHYA PRADESH	12/2009	1,352.04	1,143.54	804.28	03/2016	03/2016	0(O)	0/4
16	AMRAPALI OC(12MTY) - [N06000103]CCL, JHARKHAND	02/2012	858.11	858.11	107.24	03/2020	03/2020	0(O)	3/4

Sector Wise Details									
(July 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
17	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH	02/2015	481.60	481.60	-	03/2023	03/2023	0(O)	0/7
18	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28	207.28	191.76	03/2012	03/2017	60(O)	4/5
19	ASHOK EXPN OCP CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	341.63	341.63	124.95	03/2011	03/2017	72(O)	2/5
20	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08	172.08	148.48	03/2010	03/2017	84(O)	2/4
21	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56	258.56	84.31	03/2016	03/2016	0(O)	3/6
22	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA	05/2014	479.15	479.15	-	03/2019	03/2019	0(O)	1/9
23	BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH	09/2008	203.82	203.82	-	03/2015	03/2015	-	1/6
24	BHANEAGAN OC - [N06000121]WCL,MAHARASHTRA	02/2015	187.94	187.94	40.78	03/2023	03/2023	0(O)	5/21
25	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.10	490.10	203.68	03/2017	03/2017	0(O)	11/11
26	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL,CHHATISGARH	05/2014	164.49	164.49	76.43	03/2020	03/2020	0(O)	1/6
27	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,MADHYA PRADESH	06/2011	746.04	535.10	382.96	03/2015	03/2016	12(O)	0/3
28	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH	12/2013	610.63	610.33	-	03/2022	03/2022	0(O)	1/7
29	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35	462.35	298.70	03/2014	03/2016	24(O)	7/9
30	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51	163.51	35.92	03/2011	03/2016	60(O)	0/3
31	DINESH OCP - [N06000118]WCL,MAHARASHTRA	11/2014	611.16	611.16	6.08	03/2020	03/2020	0(O)	3/15
32	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH	12/2009	1,943.66	1,943.66	1,664.33	03/2014	03/2016	24(O)	10/13
33	GARJANBAHAL OCP - [N06000117]MCL,ODISHA	11/2014	1,375.38	1,375.38	11.77	03/2021	03/2021	0(O)	1/9
34	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67	2,675.67	1,863.12	03/2014	03/2016	24(O)	11/16
35	GOKUL - [N06000120]WCL,MAHARASHTRA	11/2014	267.67	267.67	152.29	03/2018	03/2018	0(O)	2/18
36	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,ODISHA	02/2008	395.87	395.87	76.74	03/2015	03/2021	72(O)	2/13
37	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53	479.63	173.59	03/2013	03/2017	48(O)	4/8
38	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA	05/2014	337.66	337.66	-	03/2019	03/2019	0(O)	2/6
39	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH	09/2008	152.43	152.43	24.72	03/2015	03/2020	60(O)	1/7
40	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06	447.06	29.03	03/2015	03/2018	36(O)	4/13
41	JALLARAM SHAFT PROJECT - [N06000025]SCCL,TELANGANA	09/2007	467.78	467.78	2.85	03/2013	-	-	6/83
42	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL	11/2006	287.18	287.18	225.39	03/2011	03/2017	72(O)	7/15

Sector Wise Details

(July 2015)

Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
43	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	453.63	99.71	12/2012 -	03/2017	51(O) -	11/44
44	KAKATIYAKHANI OPENCAS-2 PROJECT - [N06000129]SCCL,TELANGANA	05/2015	397.09 -	397.09	-	03/2019 -	03/2019	0(O) -	0/0
45	KALYANIKHANI OPENCAS PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	417.33	13.78	07/2016 -	03/2017	8(O) -	6/28
46	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH	12/2014	371.04 -	371.04	26.37	03/2021 -	03/2021	0(O) -	0/6
47	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	181.15	03/2013 -	03/2017	48(O) -	8/9
48	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND	08/2011	988.35 -	988.35	45.15	04/2017 04/2017	04/2017	0(O) 0(R)	0/2
49	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	-	03/2014 -	03/2017	36(O) -	3/4
50	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	0.30	03/2014 -	03/2020	72(O) -	1/7
51	KHADIA EXPANSION OPENCAS PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]NCL,UTTAR PRADESH	06/2011	1,131.28 1,131.28	1,131.28	92.65	03/2018 -	03/2018	0(O) -	0/4
52	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	242.29	0.03	03/2015 -	03/2018	36(O) -	0/5
53	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,UTTAR PRADESH	06/2011	789.88 741.62	741.62	480.93	03/2013 -	03/2016	36(O) -	0/2
54	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA	06/2014	289.03 -	289.03	-	03/2018 -	03/2018	0(O) -	1/5
55	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	146.90	03/2010 -	03/2016	72(O) -	8/10
56	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH	08/2013	7,612.33 7,612.33	7,612.33	764.69	03/2023 03/2023	03/2023	0(O) 0(R)	1/17
57	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	289.45	97.48	05/2014 -	10/2016	29(O) -	0/8
58	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	706.40 -	706.40	77.19	07/2012 -	03/2016	44(O) -	1/3
59	MAKARDHOKRA I OC - [N06000119]WCL,MAHARASHTRA	09/2014	266.23 -	266.23	81.08	03/2021 -	03/2021	0(O) -	3/22
60	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	207.27	03/2014 -	03/2016	24(O) -	4/7
61	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	181.19	36.60	03/2012 -	03/2016	48(O) -	4/6
62	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	42.39	04/2015 04/2019	04/2019	48(O) 0(R)	1/12
63	MURAIIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	10.98	04/2014 -	03/2016	23(O) -	2/5
64	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA	05/2015	295.56 -	295.56	59.83	03/2019 -	03/2019	0(O) -	4/20
65	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 -	5,907.11	1,008.61	12/2015 04/2018	04/2018	28(O) 0(R)	11/35
66	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 -	259.40	25.10	03/2012 -	03/2017	60(O) -	0/2
67	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND	02/2014	555.52 -	555.52	3.52	03/2021 -	03/2017	-48(O) -	0/2

Sector Wise Details

(July 2015)

Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
68	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87	179.87	-	03/2012	03/2017	60(O)	2/3
69	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82	269.82	40.12	04/2014	11/2016	31(O)	0/10
70	PELMA OCP(15.00MTY) - [N06000045]SECL,CHHATISGARH	11/2014	1,624.59	1,624.59	5.43	03/2023	03/2023	0(O)	1/10
71	PENGANGA OCP(REVISED) - [N06000066]WCL,MAHARASHTRA	09/2014	441.82	441.82	114.82	03/2020	03/2020	0(O)	5/27
72	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98	210.98	147.70	03/2013	03/2016	36(O)	4/4
73	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82	153.82	59.12	03/2014	03/2016	24(O)	3/9
74	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH	12/2014	357.80	357.80	108.44	03/2021	03/2021	0(O)	0/7
75	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85	510.85	223.15	03/2016	03/2016	0(O)	2/4
76	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97	418.97	365.16	03/2012	03/2016	48(O)	0/2
77	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76	162.76	1.31	03/2015	03/2019	48(O)	4/29
78	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45	486.27	71.01	03/2016	03/2016	0(O)	6/39
79	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01	365.01	6.56	06/2015	03/2016	9(O)	4/51
80	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78	209.78	74.10	03/2015	03/2016	12(O)	8/31
81	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03	249.03	73.99	03/2012	03/2018	72(O)	27/42
82	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA	05/2014	3,756.36	3,756.36	0.56	03/2026	03/2026	0(O)	3/15
83	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05	1,055.05	156.87	03/2018	03/2018	0(O)	1/10
84	TALABIRA OCP - [N06000043]MCL,ODISHA	03/2008	447.72	447.72	52.36	03/2016	03/2020	48(O)	2/11
85	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68	264.68	144.13	03/2012	03/2016	48(O)	2/4
86	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,TAMIL NADU	10/2004	2,030.78	3,583.77	3,213.77	06/2009	07/2015	73(O)	23/23
87	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,TAMIL NADU	05/2008	4,904.54	6,602.74	6,355.68	03/2012	08/2015	41(O)	32/39
88	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]NLC,TAMIL NADU	04/2012	364.75	364.75	159.12	10/2014	08/2015	10(O)	9/11
	Total		59,875.10	63,778.26	22,605.99				325/1005
	FERTILISERS								
89	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79	197.79	24.66	11/2016	11/2016	0(O)	0/0
	Total		197.79	197.79	24.66				0/0

Sector Wise Details									
(July 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>MINES</u>								
90	EXPANSION OF MALANJKHAND MINE- DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N1000007]JCL, MADHYA PRADESH	09/2011	1,856.00 -	1,856.00	-	09/2017 -	09/2017	0(O) -	0/0
	Total		1,856.00 -	1,856.00	.00				0/0
	<u>STEEL</u>								
91	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,KARNATAKA	04/2011	572.00 -	572.00	469.34	04/2013 09/2014	06/2015	-	18/19
92	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND	10/2013	245.67 -	245.67	51.94	05/2016 -	05/2016	0(O) -	1/3
93	3RD CONVERTER AND 4TH CASTER - [N12000088]RINL,ANDHRA PRADESH	07/2011	974.76 -	974.76	147.85	07/2016 -	07/2016	0(O) -	1/2
94	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,KARNATAKA	02/2011	898.55 -	898.55	390.19	05/2013 01/2015	08/2015	27(O) 7(R)	17/20
95	ALTERNATE GAS NETWORK AT BSL - [N12000093]SAIL,JHARKHAND	03/2015	255.19 -	255.19	-	03/2018 -	03/2018	0(O) -	0/0
96	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]NMDC,CHHATISGARH	01/2007	607.17 -	607.17	394.60	12/2011 01/2015	03/2015	-	20/20
97	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL,ANDHRA PRADESH	07/2011	877.73 -	877.73	263.16	07/2015 -	03/2016	8(O) -	1/2
98	CAPTIVE POWER PLANT - 2 - [N12000087]RINL,ANDHRA PRADESH	02/2011	677.00 -	677.00	523.82	09/2013 -	07/2015	22(O) -	0/1
99	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH - [N12000078]SAIL,CHHATISGARH	07/2012	332.65 -	332.65	205.40	08/2014 -	11/2015	15(O) -	4/5
100	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH	04/2014	188.93 -	188.93	32.93	04/2015 -	04/2015	-	1/4
101	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	14,537.66	03/2013 -	03/2016	36(O) -	31/35
102	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,JHARKHAND	05/2010	6,325.00 -	6,325.00	5,164.71	12/2011 -	08/2015	44(O) -	21/25
103	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL,ANDHRA PRADESH	10/2005	8,692.00 12,291.00	12,291.00	11,370.18	10/2009 10/2012	04/2015	-	69/70
104	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA	12/2011	187.33 -	187.33	163.67	10/2013 -	12/2015	26(O) -	2/6
105	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL,ODISHA	10/2012	160.48 -	160.48	132.35	09/2014 -	07/2015	10(O) -	1/3
106	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA	04/2015	3,127.30 -	3,127.30	5.18	04/2018 -	04/2018	0(O) -	0/0

Sector Wise Details									
(July 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
107	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL, JHARKHAND	05/2015	1,154.18 -	1,154.18	-	12/2017 -	12/2017	0(O) -	0/0
108	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL, JHARKHAND	03/2015	1,034.01 -	1,034.01	-	10/2017 -	10/2017	0(O) -	0/0
109	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC, CHHATISGARH	01/2010	15,525.00 -	15,525.00	7,580.18	05/2015 12/2016	12/2016	19(O) 0(R)	17/81
110	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]SAIL, WEST BENGAL	11/2012	313.05 -	313.05	267.06	06/2015 -	12/2015	6(O) -	3/4
111	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079]SAIL, ODDISHA	06/2012	237.09 -	237.09	192.84	12/2014 -	09/2015	9(O) -	1/3
112	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL, ANDHRA PRADESH	12/2009	343.00 -	488.40	25.49	10/2016 -	10/2016	0(O) -	0/0
113	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL, ANDHRA PRADESH	05/2012	404.16 -	404.16	159.15	07/2015 -	03/2017	20(O) -	0/1
114	TURBO BLOWER - 5 - [N12000092]RINL, ANDHRA PRADESH	12/2009	280.00 -	280.00	13.77	09/2016 -	09/2016	0(O) -	0/1
115	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]SAIL, ODDISHA	06/2014	708.91 -	708.91	159.27	04/2016 -	04/2016	0(O) -	2/2
	Total		61,386.16 -	65,130.56	42,250.74				210/307
	<u>PETROCHEMICALS</u>								
116	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, ASSAM	04/2006	5,460.61 8,920.00	9,833.52	8,784.45	04/2012 12/2013	09/2015	41(O) 21(R)	21/26
	Total		5,460.61 -	9,833.52	8,784.45				21/26
	<u>PETROLEUM</u>								
117	102 MW WIND POWER PROJECT - [N16000119]ONGC, RAJASTHAN	07/2010	1,106.00 678.02	678.02	405.00	06/2012 03/2015	09/2015	39(O) 6(R)	0/1
118	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]ONGC, MULTI STATE	03/2014	2,476.82 -	2,476.82	149.73	12/2018 -	12/2018	0(O) -	3/9
119	AHMEDABAD REDEVELOPMENT PROJECT - [N16000120]ONGC, GUJARAT	11/2010	1,916.10 -	1,916.10	1,161.74	12/2014 -	12/2017	36(O) -	0/0
120	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC, GUJARAT	11/2010	2,189.63 -	2,189.63	1,035.48	12/2014 -	12/2018	48(O) -	0/0
121	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, ASSAM	03/2009	2,465.15 2,378.89	2,378.89	1,781.40	03/2013 03/2016	03/2017	48(O) 12(R)	5/15
122	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL, MULTI STATE	08/2011	586.00 -	586.00	342.83	08/2015 -	12/2015	4(O) -	0/12
123	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL, MULTI STATE	01/2015	1,823.00 -	1,823.00	0.48	- -	-	-	0/0
124	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]GAIL, ANDHRA PRADESH	07/2014	419.04 -	419.04	153.06	01/2017 -	06/2016	-7(O) -	0/0
125	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS (OSV) - [N16000084]ONGC, MULTI STATE	06/2007	736.65 -	736.65	481.63	09/2011 12/2015	12/2015	51(O) 0(R)	0/0

Sector Wise Details

(July 2015)

Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
126	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC,MULTI STATE	11/2010	331.20 -	269.10	190.04	08/2013 06/2015	06/2015	-	0/0
127	CONSTRUCTION OF 6 ETSPS - [N16000117]ONGC, GUJARAT	03/2009	317.64 -	240.95	117.49	09/2012 12/2015	12/2015	39(O) 0(R)	0/5
128	CONSTRUCTION OF ONE ETP AND THREE ETSPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC, ASSAM	06/2010	202.94 188.89	188.89	2.00	01/2014 -	-	-	0/2
129	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	723.64	-	03/2013 06/2016	06/2016	39(O) 0(R)	0/0
130	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC, MAHARASHTRA	03/2011	861.79 1,256.72	1,256.72	896.92	05/2013 06/2014	12/2015	31(O) 18(R)	1/5
131	CRU TO ISOMERIZATION (ISOM) - [N16000200]BPCL,MULTI STATE	10/2011	725.00 -	725.00	23.91	11/2016 -	11/2016	0(O) -	0/0
132	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI	08/2014	6,086.08 -	6,086.08	84.54	05/2019 03/2020	03/2020	10(O) 0(R)	0/0
133	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA	12/2009	1,584.00 -	1,584.00	1,262.55	08/2015 -	12/2015	4(O) -	0/12
134	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 2,592.17	2,592.17	541.46	05/2014 05/2016	05/2016	24(O) 0(R)	0/21
135	DEVELOPMENT OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,MULTI STATE	04/2003	429.82 3,955.21	3,955.21	3,439.38	04/2006 06/2012	06/2015	-	5/5
136	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC,MULTI STATE	04/2013	284.82 -	284.82	-	04/2015 05/2017	05/2017	25(O) 0(R)	0/5
137	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17 600.17	600.17	375.14	12/2014 05/2015	05/2016	17(O) 12(R)	0/8
138	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE	06/2010	2,523.00 2,523.00	2,523.00	1,528.40	01/2014 12/2015	12/2015	23(O) 0(R)	0/13
139	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]ONGC,MULTI STATE	10/2013	429.06 429.00	429.06	357.59	10/2014 10/2015	10/2015	12(O) 0(R)	0/0
140	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL, WEST BENGAL	03/2014	3,076.00 -	3,076.00	98.00	09/2017 -	12/2017	3(O) -	0/0
141	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL, TAMIL NADU	05/2013	711.00 -	711.00	6.70	- -	-	-	0/0
142	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]ONGC, MAHARASHTRA	03/2012	5,608.40 -	5,608.40	4,456.55	05/2015 05/2015	08/2015	3(O) 3(R)	0/17
143	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]IOCL, ASSAM	02/2014	163.88 -	163.88	25.70	07/2016 -	07/2016	0(O) -	2/6
144	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC, MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	1,217.33	03/2015 05/2016	05/2016	14(O) 0(R)	0/17
145	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]ONGC, MAHARASHTRA	12/2012	3,513.07 4,619.94	4,619.94	336.33	02/2016 12/2017	12/2017	22(O) 0(R)	0/0
146	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE	05/2013	4,124.35 -	4,124.35	75.24	04/2016 04/2016	12/2017	20(O) 20(R)	0/6
147	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL, KERALA	03/2012	14,225.00 -	16,504.00	7,147.44	05/2016 -	05/2016	0(O) -	0/30
148	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE	01/2012	352.49 -	352.49	128.12	03/2014 05/2016	05/2016	26(O) 0(R)	0/3

Sector Wise Details									
(July 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
149	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE	02/2015	890.00 -	890.00	0.24	-	-	-	0/0
150	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00 -	2,915.00	1,352.10	12/2012 -	06/2015	-	0/14
151	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	12/2012	607.06 -	607.06	57.94	01/2016 -	04/2017	15(O)	11/48
152	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,KARNATAKA	02/2012	666.00 838.08	838.08	481.49	11/2015 11/2016	11/2016	12(O) 0(R)	25/29
153	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL,ODISHA	07/2009	199.75 -	239.73	192.28	07/2013 -	10/2015	27(O) -	0/1
154	MARKETING TOP AT KORBA - [N16000186]IOCL,CHHATISGARH	01/2011	141.86 -	232.00	147.60	09/2016 -	12/2015	-9(O) -	0/12
155	MEHESANA REDEVELOPMENT PROJECT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	3,823.00	1,076.57	04/2015 12/2017	12/2017	32(O) 0(R)	0/0
156	MH NORTH REDEVELOPMENT PHASE III - [N16000188]ONGC,MAHARASHTRA	06/2014	5,706.47 5,813.25	5,813.25	1,553.25	05/2017 05/2017	05/2017	0(O) 0(R)	6/16
157	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL,TAMIL NADU	12/2012	279.00 -	279.00	160.87	12/2014 -	09/2015	9(O) -	57/58
158	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA	11/2014	6,068.80 -	6,068.80	401.81	04/2019 -	03/2019	-1(O) -	0/0
159	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL,TAMIL NADU	05/2015	257.87 -	257.87	5.37	11/2016 -	11/2016	0(O) -	0/0
160	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	171.83	-	-	-	-	0/0
161	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	913.00	424.47	08/2015 -	06/2016	10(O) -	0/0
162	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00 -	2,321.00	1.50	-	-	-	0/0
163	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	-	07/2018 -	07/2018	0(O) -	0/31
164	PARADIP REFINERY PROJECT - [N16000058]IOCL,ODISHA	02/2009	29,777.00 34,555.00	34,555.00	29,606.96	11/2012 11/2013	10/2015	35(O) 23(R)	87/100
165	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	1,173.22	09/2012 -	03/2016	42(O) -	6/7
166	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]IOCL,ODISHA	03/2014	238.50 -	238.50	1.07	03/2017 -	03/2017	0(O) -	0/0
167	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	3,957.00 3,561.00	3,561.00	5.92	01/2013 -	12/2018	71(O) -	0/0
168	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT	09/2011	202.25 -	160.16	60.63	07/2016 -	07/2016	0(O) -	5/12
169	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	3,150.00	108.21	09/2017 -	09/2017	0(O) -	0/0
170	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	215.66	-	06/2012 11/2015	11/2015	41(O) 0(R)	0/0
171	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 686.58	686.58	478.03	04/2015 04/2015	12/2015	8(O) 8(R)	0/0

Sector Wise Details									
(July 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
172	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL, MAHARASHTRA	03/2012	1,419.00 -	1,419.00	1,205.72	12/2014 -	08/2015	8(O) -	0/20
173	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]IOCL, BIHAR	04/2013	480.00 -	480.00	44.48	02/2016 -	07/2016	5(O) -	2/6
174	RESID UPGRADE PROJECT - [N16000184]CPCL, TAMIL NADU	02/2011	3,110.36 -	3,110.36	799.71	11/2015 07/2016	07/2016	8(O) 0(R)	38/52
175	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL, JHARKHAND	04/2011	191.96 -	191.96	92.09	05/2015 -	12/2015	7(O) -	0/12
176	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL, GUJARAT	12/2011	160.00 -	160.00	2.47	02/2016 02/2016	02/2016	0(O) 0(R)	0/0
177	REWARI KANPUR PIPELINE PROJECT - [N16000145]HPCL, MULTI STATE	02/2012	1,210.64 1,446.34	1,446.34	1,066.43	11/2015 -	11/2015	0(O) -	18/24
178	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL, MULTI STATE	07/2011	352.56 -	450.55	10.60	03/2017 -	03/2017	0(O) -	0/0
179	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]SPRL, KARNATAKA	01/2006	732.00 1,227.00	1,227.00	979.86	10/2011 -	01/2016	51(O) -	0/0
180	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]SPRL, KERALA	01/2006	993.00 1,693.00	1,693.00	1,427.40	01/2012 -	01/2016	48(O) -	0/0
181	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]SPRL, ANDHRA PRADESH	01/2006	672.00 1,178.35	1,178.35	1,081.44	10/2011 -	06/2015	-	0/0
182	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL, ASSAM	03/2009	228.64 -	214.19	130.94	12/2016 -	12/2016	0(O) -	0/0
183	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]ONGC, TRIPURA	07/2008	288.04 253.66	253.66	229.16	08/2012 06/2015	06/2015	-	1/1
184	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL, ASSAM	09/2012	871.35 -	1,200.00	281.58	03/2015 11/2015	06/2016	15(O) 7(R)	0/5
185	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL, MULTI STATE	12/2009	309.81 462.79	462.79	237.49	10/2014 10/2016	10/2016	24(O) 0(R)	26/40
186	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL, MULTI STATE	12/2009	463.32 -	463.32	283.90	06/2011 03/2012	03/2016	57(O) 48(R)	13/20
	Total		142,903.11 -	156,858.71	72,984.98				311/700
	<u>POWER</u>								
187	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]NEEPCO, TRIPURA	07/2012	296.87 363.73	363.73	319.41	12/2014 -	05/2015	-	9/17
188	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL, MULTI STATE	03/2014	155.57 -	155.57	1.00	05/2016 -	05/2016	0(O) -	0/6
189	BARH STPP STAGE -II - [N18000047]NTPC, BIHAR	02/2008	7,341.04 10,852.46	10,852.46	8,962.00	10/2013 -	03/2015	-	20/20
190	BARH STPP(3X660MW) NTPC - [180100242]NTPC, BIHAR	02/2005	8,692.97 15,095.67	15,095.67	10,764.00	01/2011 10/2014	03/2018	86(O) 41(R)	25/48
191	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC, ASSAM	01/2008	4,375.35 6,749.18	6,749.18	5,365.00	09/2011 -	03/2017	66(O) -	15/37

Sector Wise Details

(July 2015)

Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
192	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	5,353.00	4,753.79	05/2014 -	06/2017	37(O) -	0/0
193	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	844.85	12/2015 -	06/2016	6(O) -	15/18
194	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,826.86	09/2014 -	06/2016	21(O) -	8/13
195	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	791.33	06/2015 -	08/2016	14(O) -	3/5
196	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,ANDHRA PRADESH	03/2012	206.44 -	206.44	43.97	06/2014 -	-	-	12/20
197	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	240.70	06/2015 -	08/2016	14(O) -	7/10
198	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	1,394.52	-	05/2017 -	05/2017	0(O) -	0/9
199	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL,DELHI	05/2015	780.33 -	780.33	-	07/2017 -	07/2017	0(O) -	0/0
200	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA	02/2014	12,532.44 -	12,532.44	1,713.00	08/2018 -	08/2018	0(O) -	13/14
201	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 -	195.42	29.03	02/2014 -	09/2017	43(O) -	1/1
202	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 -	196.58	1.00	02/2016 -	02/2016	0(O) -	5/17
203	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	1,127.43	11/2012 -	12/2016	49(O) -	8/13
204	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	1,364.52	278.34	04/2016 -	04/2016	0(O) -	8/12
205	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 -	522.29	30.00	11/2016 -	11/2016	0(O) -	0/12
206	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	77.53	09/2014 -	06/2016	21(O) -	0/0
207	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	197.40	-	04/2018 -	04/2018	0(O) -	0/0
208	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATTISGARH	05/2011	1,961.87 -	1,961.87	1,724.75	05/2014 -	06/2016	25(O) -	8/12
209	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH	07/2013	3,363.12 -	3,363.12	698.00	12/2016 -	12/2016	0(O) -	13/16

Sector Wise Details									
(July 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
210	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	03/2013	11,638.55 -	11,638.55	3,675.00	09/2017 -	09/2017	0(O) -	16/40
211	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]PGCIL,MULTI STATE	04/2015	1,479.30 -	1,479.30	31.40	04/2017 -	04/2017	0(O) -	0/8
212	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE	04/2015	3,705.61 -	3,705.61	57.40	04/2018 -	04/2018	0(O) -	0/9
213	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]PGCIL,MULTI STATE	05/2014	303.07 -	303.07	2.30	07/2016 -	07/2016	0(O) -	1/9
214	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24 -	1,071.24	-	10/2017 -	09/2017	-1(O) -	0/0
215	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154]PGCIL,MAHARASHTRA	10/2013	1,315.90 -	1,315.90	508.77	10/2016 -	12/2015	-10(O) -	8/10
216	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]PGCIL,MULTI STATE	12/2014	6,517.36 -	6,517.36	111.80	04/2018 -	04/2018	0(O) -	1/12
217	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,KARNATAKA	03/2005	1,007.16 -	1,007.16	1,002.91	12/2007 12/2009	12/2015	96(O) 72(R)	4/7
218	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 6,476.34	6,476.34	3,964.79	12/2009 03/2017	03/2017	87(O) 0(R)	16/29
219	KBUNL-MUZAFFARPUR TPP STAGE-II-SUBSIDIARY (2X195 MW) - [N18000191]NTPC,BIHAR	03/2010	3,984.03 -	3,984.03	2,916.06	01/2013 -	03/2016	38(O) -	0/1
220	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,497.72	4,056.08	01/2016 -	11/2016	10(O) -	4/9
221	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	01/2012	15,166.19 -	15,166.19	8,655.00	01/2017 -	01/2017	0(O) -	23/31
222	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	2,159.07	1,894.05	09/2008 03/2012	03/2016	90(O) 48(R)	20/22
223	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	12/2012	11,846.00 -	11,846.00	4,529.00	06/2017 -	06/2017	0(O) -	19/39
224	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	1,527.00	141.00	08/2017 -	08/2017	0(O) -	0/9
225	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	7,921.47	4,309.00	09/2016 -	09/2016	0(O) -	23/28
226	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	3,530.14	12/2016 -	09/2017	9(O) -	0/1
227	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 -	14,366.58	2,140.00	02/2019 -	02/2019	0(O) -	6/6
228	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	11,005.30	08/2013 -	12/2016	40(O) -	11/26
229	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL,MULTI STATE	02/2014	908.08 -	908.08	53.70	06/2016 -	06/2016	0(O) -	8/18
230	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 689.03	689.03	490.72	07/2013 05/2015	11/2015	28(O) 6(R)	7/9

Sector Wise Details									
(July 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
231	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	331.57	02/2012 -	03/2016	49(O) -	7/10
232	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	468.66	11/2011 -	03/2016	52(O) -	8/11
233	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 -	539.82	62.50	06/2016 -	06/2016	0(O) -	8/11
234	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,318.22	04/2013 -	03/2016	35(O) -	7/11
235	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	526.22	11/2014 -	12/2015	13(O) -	7/10
236	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL,MULTI STATE	09/2013	680.69 -	680.69	298.89	03/2016 -	03/2016	0(O) -	8/12
237	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	194.52	04/2015 -	09/2015	5(O) -	8/12
238	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	739.34	11/2012 -	03/2016	40(O) -	7/10
239	NPCCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 -	12,964.60	3,767.88	01/2018 -	01/2018	0(O) -	0/0
240	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]NHPC,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	-	04/2020 -	04/2020	0(O) -	0/0
241	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	7,818.68	5,142.86	09/2009 -	12/2018	111(O) -	8/14
242	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99, 1,487.49	1,487.49	1,016.43	08/2013 -	03/2016	31(O) -	28/38
243	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC, WEST BENGAL	09/2014	1,381.84 -	1,381.84	119.00	09/2019 -	09/2019	0(O) -	3/3
244	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	5,138.00	11/2016 -	08/2017	9(O) -	22/25
245	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE	05/2014	829.98 -	829.98	2.00	08/2016 -	08/2016	0(O) -	0/4
246	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]PGCIL,KARNATAKA	02/2014	167.40 -	167.40	68.80	12/2015 -	12/2015	0(O) -	5/8
247	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]PGCIL,MULTI STATE	11/2014	972.42 -	972.42	-	11/2017 -	11/2017	0(O) -	0/3
248	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	15,300.00	7,758.28	09/2010 -	-	-	0/0
249	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]PGCIL,ANDHRA PRADESH	03/2015	550.06 -	550.06	1.60	03/2018 -	03/2018	0(O) -	0/3
250	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,MULTI STATE	09/2012	1,508.74 -	1,508.74	950.08	03/2015 -	09/2015	6(O) -	15/21
251	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE	08/2014	288.49 -	288.49	23.40	02/2017 -	02/2017	0(O) -	0/12
252	SYSTEM STRENGTHENING - XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	232.34	197.99	06/2012 -	-	-	1/4

Sector Wise Details									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
253	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL,MADHYA PRADESH	03/2012	213.78 -	213.78	201.04	03/2014 -	08/2015	17(O) -	5/7
254	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHHATTISGARH - [N18000116]PGCIL,CHHATTISGARH	12/2011	1,746.65 2,228.71	2,228.71	1,265.43	08/2014 12/2015	03/2016	19(O) 3(R)	7/11
255	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,056.29	08/2012 -	03/2016	43(O) -	3/5
256	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]PGCIL,MULTI STATE	02/2014	243.53 -	243.53	146.50	08/2016 -	08/2016	0(O) -	8/10
257	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 -	203.28	0.20	07/2017 -	07/2017	0(O) -	0/5
258	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATTISGARH	01/2012	1,422.85 -	1,422.85	1,181.42	01/2015 -	03/2016	14(O) -	9/11
259	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 346.79	346.79	285.47	08/2014 06/2015	12/2015	16(O) 6(R)	8/10
260	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	487.49	379.02	06/2014 -	11/2015	17(O) -	8/12
261	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH	09/2014	9,188.98 -	9,188.98	717.00	03/2019 -	03/2019	0(O) -	7/12
262	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	2,512.00	03/2013 -	12/2018	69(O) -	1/15
263	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]NHPC, WEST BENGAL	09/2005	1,061.38 -	1,929.15	1,813.21	09/2009 -	06/2016	81(O) -	2/6
264	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	1,335.62	07/2010 02/2016	05/2018	94(O) 27(R)	6/21
265	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL- PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	2,085.56	08/2014 -	09/2015	13(O) -	8/14
266	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAND AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	2,456.41	10/2014 -	03/2016	17(O) -	8/17
267	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	4,133.98	10/2012 -	03/2016	41(O) -	7/11
268	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]PGCIL, GUJARAT	02/2014	378.71 -	378.71	81.90	10/2016 -	10/2016	0(O) -	8/11
269	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]PGCIL,MULTI STATE	01/2015	268.80 -	268.80	0.80	03/2018 -	03/2018	0(O) -	0/3
270	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL,MULTI STATE	02/2012	1,927.16 -	1,927.16	1,533.67	10/2014 -	09/2015	11(O) -	11/15
271	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]PGCIL,MULTI STATE	06/2014	400.47 -	400.47	10.40	04/2017 -	04/2017	0(O) -	0/3
272	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL,MULTI STATE	09/2013	1,575.30 -	1,575.30	370.20	05/2016 -	05/2016	0(O) -	8/13

Sector Wise Details									
(July 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
273	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	2,176.10	12/2012 -	03/2016	39(O) -	11/23
274	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE	01/2015	871.62 -	871.62	1.90	11/2017 -	11/2017	0(O) -	0/5
275	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]PGCIL,ANDHRA PRADESH	08/2014	188.75 -	188.75	1.00	02/2017 -	02/2017	0(O) -	0/2
276	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	529.30	02/2014 -	09/2015	19(O) -	8/10
277	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 -	4,404.57	1,959.15	01/2015 -	03/2016	14(O) -	8/16
278	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	464.61	11/2013 -	12/2015	25(O) -	8/12
279	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 2,348.37	2,348.37	1,878.34	03/2013 06/2015	10/2015	31(O) 4(R)	8/11
280	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]PGCIL,MULTI STATE	03/2011	2,569.25 3,105.51	3,105.51	2,854.67	03/2014 06/2015	08/2015	17(O) 2(R)	10/13
281	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19 -	2,743.19	2,783.30	12/2013 -	09/2015	21(O) -	9/11
282	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	142.10	01/2013 -	09/2015	32(O) -	10/15
283	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,492.46	11/2013 -	12/2015	25(O) -	8/12
284	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I) - [N18000198]PGCIL,ANDHRA PRADESH	05/2015	312.94 -	312.94	-	06/2016 -	05/2016	-1(O) -	0/0
285	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. - [N18000076]PGCIL,MULTI STATE	03/2010	4,672.99 -	4,672.99	3,756.67	11/2012 -	08/2015	33(O) -	8/13
286	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH	11/2011	2,127.51 -	2,127.51	2,211.93	07/2014 -	03/2016	20(O) -	6/8
287	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	5,151.37	488.30	03/2018 -	03/2018	0(O) -	8/12
288	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 1,007.68	1,007.68	902.86	07/2013 -	08/2015	25(O) -	25/26
289	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM	07/1998	368.72 1,381.71	1,381.71	857.94	07/2006 12/2015	10/2016	123(O) 10(R)	5/13

Sector Wise Details									
(July 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
290	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL, MULTI STATE	01/2014	374.63 -	374.63	-	04/2016 -	11/2016	7(O) -	0/0
291	VINDHYACHAL STPP STAGE-V - [N18000134]NTPC,MADHYA PRADESH	05/2012	3,180.40 -	3,180.40	1,981.00	08/2015 -	08/2015	0(O) -	28/28
292	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	3,745.08	701.40	06/2013 -	12/2019	78(O) -	2/8
293	WARDHA-HYDERABAD 765 KV LINK - [N18000183]PGCIL,MULTI STATE	01/2015	3,662.02 -	3,662.02	62.90	05/2018 -	05/2018	0(O) -	0/5
294	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 721.81	721.81	521.59	09/2010 06/2013	03/2016	66(O) 33(R)	4/8
295	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATTISGARH	03/2012	9,569.76 -	9,569.76	4,720.39	06/2015 -	06/2016	12(O) -	20/30
	Total		309,271.77 -	349,101.15	172,846.68				779/1338
	<u>HEAVY INDUSTRY</u>								
296	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]HIPE,MULTI STATE	04/2011	1,718.00 -	3,827.30	-	09/2011 -	12/2017	75(O) -	0/0
	Total		1,718.00 -	3,827.30	.00				0/0
	<u>RAILWAYS *</u>								
297	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MTRP,TELANGANA	04/2012	632.68 -	816.55	-	03/2016 -	03/2016	0(O) -	0/0
298	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	184.06	15.23	- -	-	-	0/0
299	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 813.34	2,876.00	823.83	03/2014 -	03/2018	48(O) -	0/0
300	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	252.00 -	886.65	-	- -	03/2018	-	0/0
301	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	432.72	436.85	12/2009 03/2011	06/2015	-	0/0
302	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	567.18	31.99	- -	-	-	0/0
303	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	385.60	83.50	03/2013 -	-	-	0/0
304	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	2,820.00	329.67	- -	-	-	0/0
305	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	873.71	-	- -	-	-	0/0
306	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	218.39	23.63	- -	-	-	0/0
307	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	822.00	-	- -	-	-	0/0
308	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE	04/2008	184.26 -	2,000.00	17.32	- -	-	-	0/0

Sector Wise Details

(July 2015)

Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
309	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE	12/2006	170.00	485.00	417.70	03/2011	-	-	0/0
310	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09	242.09	0.39	-	-	-	0/0
311	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54	338.54	129.14	-	-	-	0/0
312	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	312.12	453.10	134.79	-	03/2018	-	0/0
313	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01	725.00	586.75	06/1999	07/2012	-	0/0
314	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68	295.68	0.86	-	-	-	0/0
315	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00	307.00	-	-	-	-	0/0
316	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00	1,566.00	137.40	-	-	-	0/0
317	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80	490.80	0.39	-	-	-	0/0
318	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41	304.41	0.19	-	-	-	0/0
319	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA	03/2015	960.00	960.00	-	-	-	-	0/0
320	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87	528.00	2.96	-	-	-	0/0
321	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75	199.75	76.08	-	-	-	0/0
322	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93	986.30	100.76	-	-	-	0/0
323	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35	288.35	9.60	-	-	-	0/0
324	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52	207.52	223.44	12/2012	09/2015	33(O)	0/0
325	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00	1,382.78	2.81	-	-	-	0/0
326	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08	246.08	4.20	-	-	-	0/0
327	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,WEST BENGAL	03/1998	111.90	2,371.85	486.25	03/2005	12/2019	177(O)	0/0
328	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	1,106.62	1,106.62	244.99	12/2010	-	132(R)	0/0
329	BARIAPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55	450.55	13.53	-	-	-	0/0
330	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64	255.64	-	-	-	-	0/0
331	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44	1,781.98	440.08	03/2004	03/2016	144(O)	0/0
332	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49	337.50	0.21	-	-	-	0/0

Sector Wise Details									
(July 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
333	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	923.23	1.01	-	-	-	0/0
334	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 -	837.33	1.15	-	-	-	0/0
335	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL	04/2011	289.64 -	760.00	0.09	-	-	-	0/0
336	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34 619.34	2,820.25	199.31	04/2014 03/2015	03/2018	47(O) 36(R)	0/0
337	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	2,966.99	40.80	-	-	-	0/0
338	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	196.95	198.83	03/2011 -	-	-	0/0
339	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	195.64	94.11	-	-	-	0/0
340	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	800.00	793.71	03/2010 -	12/2015	69(O) -	0/0
341	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	321.62	2.91	03/2012 -	-	-	0/0
342	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	326.20	1.68	-	-	-	0/0
343	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	175.80	1.46	-	-	-	0/0
344	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	434.00	35.90	-	-	-	0/0
345	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 1,000.00	4,996.19	3,410.06	04/2008 03/2014	06/2017	110(O) 39(R)	0/0
346	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	579.37	599.40	-	02/2012	-	0/0
347	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	230.00	68.67	03/2015 -	12/2016	21(O) -	0/0
348	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	328.14	0.30	-	-	-	0/0
349	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	337.96	61.36	-	-	-	0/0
350	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00 -	951.24	619.87	-	03/2015	-	0/0
351	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	222.95	112.40	-	-	-	0/0
352	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	520.00	462.69	-	-	-	0/0
353	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	1,200.00	2.07	-	-	-	0/0
354	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	494.92	4.22	-	-	-	0/0
355	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	378.56	111.87	-	-	-	0/0

Sector Wise Details									
(July 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
356	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 663.67	1,101.16	194.91	- -	03/2017	- -	0/0
357	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	243.78	30.05	- -	-	-	0/0
358	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	367.77	-	- -	-	-	0/0
359	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	692.43	-	- -	-	-	0/0
360	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	595.91	89.60	- -	-	-	0/0
361	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	1,347.26	164.55	- -	-	-	0/0
362	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	573.78	166.89	- -	-	-	0/0
363	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 575.00	1,242.25	1,005.81	03/2007 -	03/2016	108(O) -	0/0
364	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	556.64	268.56	- -	-	-	0/0
365	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	829.00	-	- -	-	-	0/0
366	CUTTACK - BARANG (LD) - [220100326]RVNL,ODISHA	04/1995	127.13 -	225.00	193.37	- 10/2014	10/2014	-	0/0
367	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	1,640.04	187.84	- -	-	-	0/0
368	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	533.38 -	533.38	114.38	12/2011 -	-	-	0/0
369	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	968.60	-	12/2012 -	-	-	0/0
370	DANGOPOSI-RAJIKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	583.00	144.66	12/2015 -	03/2016	3(O) -	0/0
371	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	339.00	204.83	- -	-	-	0/0
372	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	296.44	4.55	- -	-	-	0/0
373	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	205.00	5.21	- -	-	-	0/0
374	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	410.08	297.58	- -	-	-	0/0
375	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	234.71	137.01	03/2015 -	03/2015	-	0/0
376	DELHI-SOHA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	1,239.00	-	- -	-	-	0/0
377	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	336.91	144.25	- -	-	-	0/0
378	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	607.09	561.14	12/2012 12/2012	-	-	0/0

Sector Wise Details									
(July 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
379	DHASA-JETALSAR (GC) - [N22000141]WR, GUJARAT	04/2012	376.59 -	376.59	4.58	- -	-	-	0/0
380	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]NCR, MULTI STATE	04/2010	622.41 2,030.50	2,030.50	3.61	02/2019 -	02/2019	0(O) -	0/0
381	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER, MULTI STATE	04/2010	553.63 651.17	1,009.00	7.50	- -	12/2019	- -	0/0
382	DIMAPUR-TIZIT NL - [N22000196]NFR, NAGALAND	04/2013	4,274.00 -	4,487.70	-	- -	03/2020	- -	0/0
383	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR, TAMIL NADU	09/2006	343.17 -	914.98	846.18	- -	03/2016	- -	0/0
384	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	4,874.58	1,911.65	03/2016 -	06/2018	27(O) -	0/0
385	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE, UTTAR PRADESH	02/2008	171.10 236.37	275.08	141.55	03/2012 12/2013	03/2016	48(O) 27(R)	0/0
386	ERNAKULAM-KUMBALAM - [N22000204]SR, KERALA	04/2010	189.24 -	189.24	1.52	- -	-	-	0/0
387	ERODE-PALANI - [N22000199]SR, TAMIL NADU	04/2008	288.57 -	603.22	1.64	- -	-	-	0/0
388	ETAWAH-MAINPURI (NL), NCR - [220100318]NCR, UTTAR PRADESH	04/1997	120.00 245.39	245.39	249.33	12/2008 -	10/2015	82(O) -	0/0
389	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP, TAMIL NADU	04/2006	495.74 -	495.74	315.66	06/2013 06/2013	06/2013	-	0/0
390	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR, UTTAR PRADESH	04/2013	654.00 -	654.00	-	- -	-	-	0/0
391	GADAG-WADI NL - [N22000299]SWR, KARNATAKA	04/2013	1,117.00 -	1,922.00	1.89	- -	-	-	0/0
392	GADWAL - RAICHUR (NL), SCR - [220100270]SCR, MULTI STATE	04/1998	92.63 -	270.00	301.84	02/2011 02/2011	-	-	0/0
393	GAYA-CHATRA (NL) - [N22000169]ECOR, MULTI STATE	04/2008	415.67 -	415.67	14.00	- -	-	-	0/0
394	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR, BIHAR	04/2008	445.25 -	445.25	1.14	- -	-	-	0/0
395	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER, UTTAR PRADESH	04/2014	182.92 -	197.73	-	- -	-	-	0/0
396	GHUTIA SHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL	04/2009	611.03 -	611.03	140.48	12/2011 11/2013	11/2013	-	0/0
397	GOELKERA-MANOHARPUR, (LD)(SER) - [N22000045]SER, JHARKHAND	03/1997	261.70 -	280.00	-	02/2006 -	-	-	0/0
398	GONDIA-JABALPUR (GC), (SECR) - [220100186]SECR, MULTI STATE	02/1997	386.30 1,157.54	1,544.40	590.26	03/1998 -	12/2019	261(O) -	0/0
399	GRADE SEPARATOR AT DAYABASTI - [N22000269]NR, DELHI	04/1999	156.65 -	156.65	53.00	- -	-	-	0/0
400	GUDUR-DURGARA JAPATNAM - [N22000265]SCR, ANDHRA PRADESH	04/2011	283.54 -	283.54	0.31	- -	-	-	0/0
401	GULBARGA-BIDAR, SCR (NL) - [220100254]SCR, KARNATAKA	02/1998	242.42 369.70	844.00	798.87	- 05/2009	03/2015	-	0/0

Sector Wise Details									
(July 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
402	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	608.02	602.10	03/1994 -	03/2015	-	0/0
403	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	179.32	75.76	- -	-	-	0/0
404	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 3,845.60	3,845.60	2.33	02/2020 -	02/2020	0(0) -	0/0
405	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	157.17	76.90	- -	-	-	0/0
406	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	720.00 -	720.00	-	- -	-	-	0/0
407	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	367.17	17.19	- -	-	-	0/0
408	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	324.66	227.03	- -	-	-	0/0
409	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	267.09	1.50	- -	-	-	0/0
410	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	172.03	5.86	- -	-	-	0/0
411	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	1,185.64	-	- 09/2009	-	-	0/0
412	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	329.97	2.38	- -	-	-	0/0
413	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 -	1,289.92	1,092.98	- -	-	-	0/0
414	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	230.03	172.58	- -	-	-	0/0
415	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	829.74	96.76	03/2015 -	03/2015	-	0/0
416	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	400.00	-	- -	-	-	0/0
417	HOSADURGA - CHICKJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA	04/2010	203.40 -	203.40	153.29	- -	09/2015	-	0/0
418	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	2,127.00	325.00	- -	-	-	0/0
419	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 -	1,618.00	-	- -	-	-	0/0
420	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	157.94	43.34	- -	-	-	0/0
421	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 393.46	1,026.00	181.48	03/2007 03/2007	03/2015	-	0/0
422	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	166.89	0.02	- -	-	-	0/0
423	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,900.00 -	1,900.00	-	- -	-	-	0/0
424	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	2,135.00	117.24	- -	-	-	0/0

Sector Wise Details

(July 2015)

Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
425	JAGGAYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24	313.24	230.62	01/1999	-	-	0/0
426	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19	653.55	258.78	03/2014	-	-	0/0
427	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96	162.96	143.62	-	-	-	0/0
428	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30	847.75	835.14	06/2007	-	-	0/0
429	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69	1,043.56	819.19	03/2012	-	-	0/0
430	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00	470.00	40.00	-	-	-	0/0
431	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00	230.00	218.67	-	-	-	0/0
432	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56	740.00	639.77	03/2012	12/2012	-	0/0
433	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56	6,570.75	2,787.99	03/2011	03/2019	96(O)	0/0
434	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00	2,050.00	194.45	-	-	-	0/0
435	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52	923.52	208.10	-	-	-	0/0
436	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56	174.56	63.08	-	-	-	0/0
437	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70	279.70	4.73	-	-	-	0/0
438	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97	1,651.54	1,621.40	-	03/2018	-	0/0
439	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00	643.00	-	-	-	-	0/0
440	KAPTANGANJ-THAWA-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	744.71	744.71	576.86	-	03/2016	-	1/1
441	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55	800.00	800.70	-	-	-	0/0
442	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM	04/1998	227.90	331.40	182.22	12/2012	03/2016	39(O)	0/0
443	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98	1,727.27	743.74	12/2010	03/2018	87(O)	0/0
444	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66	423.66	163.59	03/2017	03/2017	0(O)	0/0
445	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35	1,054.35	8.06	-	-	-	0/0
446	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87	541.00	158.58	-	-	-	0/0

Sector Wise Details									
(July 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
447	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	276.00	-	03/2009 03/2009	08/2014	-	0/0
448	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	1,995.25	355.02	- -	-	-	0/0
449	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 -	1,143.60	189.12	- -	03/2018	-	0/0
450	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	282.92 282.92	565.13	2.80	- 03/2014	03/2018	- 48(R)	0/0
451	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87 -	768.87	682.31	- 03/2010	03/2010	-	0/0
452	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	2,957.21 -	2,957.21	1,966.90	07/2005 -	-	-	0/0
453	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	418.17	260.67	- -	-	-	0/0
454	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE	04/2013	723.00 -	723.00	-	- -	-	-	0/0
455	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	341.41	325.36	03/2012 -	-	-	0/0
456	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	1,047.00	1.29	- -	-	-	0/0
457	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	252.96	1.48	- -	-	-	0/0
458	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	192.56	0.38	- -	-	-	0/0
459	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	346.15	14.61	- -	-	-	0/0
460	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	406.99	141.55	- -	-	-	0/0
461	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	1,630.97	488.76	05/2008 -	-	-	0/0
462	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	257.42	67.97	03/2014 -	03/2014	-	0/0
463	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM	04/2012	246.07 246.07	364.06	0.30	- -	03/2019	-	0/0
464	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 -	5,500.00	4,734.45	03/2009 -	03/2016	84(O) -	0/0
465	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	480.00	3.51	07/2008 -	07/2008	-	0/0
466	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	450.00	16.97	- -	-	-	0/0
467	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	800.00	0.69	- -	-	-	0/0
468	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	493.96	121.27	- -	-	-	0/0
469	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	343.00	216.17	- -	-	-	0/0

Sector Wise Details									
(July 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
470	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	900.05	853.83	12/2011 12/2010	-	-	0/0
471	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	378.56 -	791.59	5.41	-	-	-	0/0
472	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 315.13	365.00	2.52	-	12/2017	-	0/0
473	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	369.00	188.93	-	-	-	0/0
474	MANSI-PURNA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 332.92	477.88	498.37	03/2012 -	-	-	0/0
475	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	1,112.00	-	-	-	-	0/0
476	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	279.54	1.38	01/1999 -	-	-	0/0
477	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	855.16	557.82	-	-	-	0/0
478	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	1,383.45	457.88	-	-	-	0/0
479	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	377.44	7.50	-	-	-	0/0
480	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 -	1,830.00	-	-	-	-	0/0
481	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	439.88	0.78	-	-	-	0/0
482	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	800.00	0.83	01/1999 -	-	-	0/0
483	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	426.00	-	01/1999 -	-	-	0/0
484	MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	250.93	0.14	-	-	-	0/0
485	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	926.09	4.41	-	-	-	0/0
486	MUDKHED-PARBHANI - [N22000283]SCR,MAHARASHTRA	04/2011	390.60 -	390.60	4.69	-	-	-	0/0
487	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 6,821.29	7,986.04	2,443.62	03/2014 03/2019	03/2019	60(O) 0(R)	0/0
488	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 236.41	645.00	309.19	-	03/2015	-	0/0
489	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	1,350.91	380.62	-	-	-	0/0
490	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	165.82 165.82	435.58	0.56	-	03/2018	-	0/0
491	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	281.30	0.58	-	-	-	0/0
492	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	228.05	1.52	-	-	-	0/0
493	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	1,313.48	5.13	-	-	-	0/0

Sector Wise Details									
(July 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
494	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	883.00	755.50	02/2009 -	03/2015	-	0/0
495	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	2,100.00	391.95	07/2012 -	-	-	0/0
496	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	620.57	-	- -	-	-	0/0
497	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	494.54	31.20	- -	-	-	0/0
498	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	300.00 300.00	827.73	53.52	- -	03/2019	-	0/0
499	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	200.00 200.00	496.24	213.72	- -	03/2017	-	0/0
500	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 171.00	679.57	40.41	- -	03/2018	-	0/0
501	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	4,083.02 -	5,307.90	7.79	- 03/2016	03/2020	- 48(R)	0/0
502	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 210.00	394.28	233.46	- -	03/2017	-	0/0
503	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL	04/2010	221.42 205.31	563.13	22.39	- -	03/2019	-	0/0
504	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	36.80 36.38	1,336.57	255.55	- -	03/2019	-	0/0
505	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 1,798.00	1,887.90	-	- -	03/2019	-	0/0
506	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR,WEST BENGAL	04/2011	209.77 190.39	441.45	85.78	- -	03/2018	-	0/0
507	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR,WEST BENGAL	04/2012	283.55 278.21	288.81	11.74	- -	03/2018	-	0/0
508	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL & RAJABHATKHOWA-JAI - [N22000209]NFR,MULTI STATE	04/1999	523.17 380.60	1,653.55	1,040.11	- -	03/2018	-	0/0
509	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00 -	2,973.42	10.44	03/2015 03/2020	03/2020	60(O) 0(R)	0/0
510	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	733.00 733.00	2,531.34	1,732.43	12/2008 -	03/2018	111(O) -	0/0
511	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,069.60	-	03/2014 -	-	-	0/0
512	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	2,619.02	-	03/2016 -	03/2016	0(O) -	0/0
513	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	204.56	03/2016 -	06/2016	3(O) -	0/0

Sector Wise Details									
(July 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
514	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	3,951.98	-	03/2016 -	03/2016	0(O) -	0/0
515	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, ANDHRA PRADESH	07/2006	743.00 -	1,117.11	-	03/2008 06/2008	-	-	0/0
516	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR, GUJARAT	04/2013	1,266.89 -	1,266.89	-	-	-	-	0/0
517	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	293.74 -	293.74	140.08	12/2010 -	-	-	0/0
518	PANVEL PEN DOUBLING - [N22000255]CR, MULTI STATE	04/2006	96.16 -	260.16	240.21	-	01/2015	-	0/0
519	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR, BIHAR	04/2001	624.47 -	2,921.00	2,521.72	10/2007 12/2012	12/2015	98(O) 36(R)	0/0
520	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, TELANGANA	12/1994	124.43 -	925.30	712.02	-	02/2014	-	0/0
521	PEN ROHA DOUBLING - [N22000254]CR, MULTI STATE	04/2007	98.74 -	203.00	227.84	-	03/2015	-	0/0
522	PHULERA - DIGANA DOUBLING - [N22000326]NWR, MULTI STATE	05/2015	600.00 -	600.00	-	-	-	-	0/0
523	PIRPAINTI-BHAGALPUR - [N22000222]ER, MULTI STATE	04/2011	261.38 -	261.38	21.21	-	-	-	0/0
524	PIRPAINTI-JASIDIH - [N22000219]ER, MULTI STATE	04/2013	915.98 -	915.98	0.09	-	-	-	0/0
525	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER, MULTI STATE	04/2011	248.07 -	248.07	29.10	03/2015 -	03/2015	-	0/0
526	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER, MULTI STATE	04/2011	299.60 -	299.60	1.10	03/2017 -	03/2017	0(O) -	0/0
527	PUSHKAR-MERTA - [N22000151]NWR, RAJASTHAN	04/2013	323.00 -	323.00	-	-	-	-	0/0
528	QADIAN-BEAS - [N22000295]NR, PUNJAB	04/2011	205.22 -	205.22	1.54	-	-	-	0/0
529	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR, TAMIL NADU	04/1999	460.94 -	1,030.00	800.90	01/1999 -	-	-	0/0
530	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR, MULTI STATE	03/1998	280.00 -	1,122.00	889.95	-	-	-	0/6
531	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL, ANDHRA PRADESH	04/2003	136.62 -	289.93	-	12/2007 03/2010	-	-	0/0
532	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR, BIHAR	04/2002	921.00 -	2,363.00	1,691.12	03/2009 12/2012	10/2015	79(O) 34(R)	0/0
533	RAJATGARH-BARANG(LD), ECR - [220100286]RVNL, ODISHA	04/1999	166.16 -	288.00	-	02/2009 02/2009	08/2014	-	0/0
534	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER, JHARKHAND	04/2012	148.77 -	209.00	2.64	12/2016 -	12/2016	0(O) -	0/0
535	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR, GUJARAT	04/1994	320.66 913.48	913.48	457.67	-	-	-	0/0
536	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR, KARNATAKA	04/2007	482.00 -	874.57	730.11	03/2013 -	09/2015	30(O) -	0/0

Sector Wise Details									
(July 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
537	RAMGANJIMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	470.92 727.13	1,225.90	257.59	- -	03/2017	- -	0/0
538	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	335.00	230.67	06/2004 -	12/2015	138(O) -	0/0
539	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	288.97	1.09	- -	-	-	0/0
540	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	872.22	794.11	- -	-	-	0/0
541	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	3,500.00	54.23	- -	-	-	0/0
542	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	1,421.25	420.33	03/2012 -	-	-	0/0
543	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	1,743.00	359.06	- -	-	-	0/0
544	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA	05/2015	400.00 -	400.00	-	- -	-	-	0/0
545	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	576.18	3.40	- -	-	-	0/0
546	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	714.10	65.93	04/2016 -	03/2017	11(O) -	0/0
547	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	193.44	53.01	- -	-	-	0/0
548	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	325.00	258.31	- -	-	-	0/0
549	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	355.81	294.07	- -	-	-	0/0
550	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	385.54	-	03/2010 -	-	-	0/0
551	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	380.00	-	- -	-	-	0/0
552	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	155.81	18.25	- -	12/2016	- -	0/0
553	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 -	1,111.99	60.31	- -	-	-	0/0
554	SANTOSHUPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	268.52	78.81	- -	-	-	0/0
555	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 1,339.48	4,190.00	88.56	12/2015 -	03/2020	51(O) -	0/0
556	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	832.47	0.94	- -	-	-	0/0
557	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	239.32	17.17	- -	-	-	0/0
558	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	297.47	51.82	- -	-	-	0/0
559	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	277.28	67.82	- -	-	-	0/0

Sector Wise Details									
(July 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
560	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	466.65	-	-	-	-	0/0
561	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	1,500.00	0.01	-	-	-	0/0
562	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	818.29	-	02/2015 -	-	-	0/0
563	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	450.00	7.91	-	-	-	0/0
564	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 732.06	516.23	597.72	03/2014 -	-	-	0/0
565	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	810.80	160.80	-	-	-	0/0
566	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 1,013.74	1,428.00	466.36	06/2005 07/2011	12/2019	174(O) 101(R)	0/0
567	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	171.02 -	171.00	166.84	06/2013 -	01/2015	-	0/0
568	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	365.17	1.35	-	-	-	0/0
569	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	1,188.91	687.63	- 12/2009	-	-	0/0
570	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR,TAMIL NADU	04/2011	190.10 -	190.10	33.19	-	-	-	0/0
571	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	262.00	0.41	-	-	-	0/0
572	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 -	1,080.00	194.61	-	-	-	0/0
573	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 -	490.00	67.57	-	-	-	0/0
574	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	167.73	124.14	03/2012 -	-	-	0/0
575	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 -	980.00	596.66	-	-	-	0/0
576	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 3,385.14	3,404.92	3,551.53	12/2006 -	-	-	0/0
577	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	167.50	0.32	-	-	-	0/0
578	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	1,801.01	1.47	-	-	-	0/0
579	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	19,565.00	10,658.34	11/2002 -	12/2018	193(O) -	0/0
580	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	1,389.62	1,055.80	03/2014 -	-	-	0/0
581	UNCHAHR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	380.00	1.38	-	-	-	0/0
582	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 -	1,564.54	420.71	03/2010 03/2017	03/2017	84(O) 0(R)	0/0

Sector Wise Details

(July 2015)

Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
583	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	-	-	-	-	0/0
584	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	1,280.83	1,031.83	-	-	-	0/0
585	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 -	548.01	201.26	-	-	-	0/0
586	VIRAMGAM-SAMAKHALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	685.17	206.59	-	-	-	0/0
587	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	279.40	249.02	-	-	-	0/0
588	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	2,501.05	84.11	-	-	-	0/0
589	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	297.85	7.17	-	-	-	0/0
590	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	348.85	0.34	-	-	-	0/0
591	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	876.00	-	-	-	-	0/0
592	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	860.43	-	-	-	-	0/0
	Total		171,881.41 -	296,947.84	87,417.33				1/7
	ROAD TRANSPORT AND HIGHWAYS								
593	2 LANING OF DINDIGUL - PERIGULAM THENI-KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	-	08/2013	-	-	0/0
594	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH	10/2012	250.50 -	250.50	65.26	10/2014	-	-	0/0
595	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	373.47	-	07/2014	-	-	0/0
596	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	351.54	-	05/2013	-	-	0/0
597	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	-	11/2013	-	-	0/0
598	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	624.00	-	04/2014	07/2015	15(O)	0/0
599	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	356.40	-	07/2014	-	-	0/0
600	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI,RAJASTHAN	03/2014	240.10 -	240.10	-	03/2016	03/2016	0(O)	0/0
601	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR - [N24000238]NHAI,RAJASTHAN	01/2014	158.04 -	158.04	2.67	12/2015	12/2015	0(O)	0/0
602	2-LANING WITH PS OF JHALAWAR-RAJASTHAN-MP. BORDER - [N24000237]NHAI,RAJASTHAN	01/2014	177.32 -	177.32	86.65	01/2016	01/2016	0(O)	0/0
603	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	-	01/2014	-	-	0/0
604	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	226.00	282.30	02/2014	02/2014	-	0/0

Sector Wise Details									
(July 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
605	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, BIHAR	05/2011	664.00 -	664.00	-	02/2014 -	-	-	0/0
606	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, BIHAR	10/2011	375.09 -	375.09	-	04/2014 -	-	-	0/0
607	2LANING WITH PS GOPALGANJ-CHAPPRA - [N24000190]NHAI, BIHAR	12/2011	325.00 -	325.00	160.20	05/2014 -	05/2014	-	0/0
608	4 - LANNING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236]NHAI, RAJASTHAN	10/2013	677.79 -	677.79	59.09	04/2016 -	04/2016	0(0) -	0/0
609	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI, GUJARAT	03/2012	828.00 -	828.00	-	09/2014 -	-	-	0/3
610	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI, MULTI STATE	02/2011	2,498.76 -	2,498.76	-	08/2014 -	-	-	0/0
611	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI, GUJARAT	12/2010	1,008.50 -	1,008.50	-	06/2013 -	-	-	0/3
612	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI, KARNATAKA	03/2011	359.00 -	359.00	-	09/2013 -	-	-	0/0
613	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI, GUJARAT	03/2011	785.50 -	785.50	-	08/2013 -	-	-	0/3
614	4 LANNING OF BRAHAMPUR-BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI, TELANGANA	04/2014	1,266.60 -	1,266.60	-	09/2016 -	09/2016	0(0) -	0/0
615	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI, JHARKHAND	02/2012	398.00 -	398.00	344.40	02/2014 -	09/2015	19(0) -	0/0
616	4-LANING OF BRAHAMPUR-FARAKA - [N24000203]NHAI, MULTI STATE	02/2011	998.79 -	998.79	-	08/2013 -	-	-	0/0
617	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, MULTI STATE	02/2011	1,078.84 -	1,078.84	-	08/2013 -	-	-	0/0
618	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI, MULTI STATE	02/2011	580.43 -	580.43	-	08/2013 -	-	-	0/0
619	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI, HARYANA	10/2013	283.25 -	283.25	-	10/2015 -	10/2015	0(0) -	0/0
620	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, BIHAR	01/2011	575.00 -	575.00	-	07/2013 -	-	-	0/0
621	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	1,396.18	-	09/2014 -	-	-	0/0
622	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI, UTTAR PRADESH	12/2003	348.16 -	348.16	269.40	09/2007 -	-	-	0/0
623	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI, GUJARAT	01/2013	2,125.24 -	2,125.24	163.30	12/2015 -	12/2015	0(0) -	0/3
624	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI, TELANGANA	02/2010	390.56 -	390.56	631.70	02/2012 -	06/2013	-	0/0
625	BAREILLY-SITAPUR (NH-24) - [N24000200]NHAI, UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	-	09/2013 -	-	-	0/0
626	BARSAT-KRISHNANAGAR - [N24000229]NHAI, WEST BENGAL	08/2012	867.00 -	867.00	-	02/2015 -	-	-	0/0
627	BEAWAR-PALI-PINDWARA - [N24000199]NHAI, RAJASTHAN	12/2011	2,388.00 -	2,388.00	2,301.00	06/2014 -	11/2015	17(0) -	0/0
628	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI, KARNATAKA	12/2010	480.00 -	480.00	-	-	-	-	2/2
629	BHOPAL-SANCHI - [N24000192]NHAI, MADHYA PRADESH	10/2011	209.00 -	209.00	11.28	01/2013 -	12/2015	35(0) -	0/0

Sector Wise Details									
(July 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
630	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	500.29	-	08/2013 -	-	-	0/0
631	BIJNI TO ASSAM /WB BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	237.80	-	06/2008 -	-	-	0/0
632	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	195.00	-	06/2008 -	-	-	0/0
633	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	230.00	-	06/2005 -	-	-	0/0
634	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	309.56	-	04/2010 01/2016	01/2016	69(O) 0(R)	0/0
635	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	281.31	-	02/2010 -	-	-	0/0
636	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	-	03/2013 -	-	-	0/0
637	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	353.37	-	10/2011 -	-	-	0/0
638	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	572.30	-	10/2011 -	-	-	0/0
639	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	-	05/2013 -	-	-	0/0
640	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	300.00	176.80	10/2008 -	-	-	0/0
641	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	1,928.22	-	04/2015 -	04/2015	-	0/0
642	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	-	05/2010 -	-	-	0/0
643	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	593.00	-	07/2013 -	-	-	0/0
644	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	-	06/2013 -	-	-	0/0
645	DEVIHALLI-HASSAN - [N24000152]NHAI,KARNATAKA	12/2010	453.00 -	453.00	-	- -	-	-	1/1
646	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	200.00	289.50	06/2008 -	05/2015	-	0/0
647	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	-	05/2008 10/2015	10/2015	89(O) 0(R)	0/0
648	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	232.45	-	09/2010 -	-	-	0/0
649	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	1,573.00	-	09/2015 -	09/2015	0(O) -	0/0
650	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	332.94	-	09/2008 -	-	-	0/0
651	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	1,916.79	-	11/2016 -	11/2016	0(O) -	0/0
652	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00 -	1,232.00	590.90	08/2015 -	02/2016	6(O) -	0/0

Sector Wise Details									
(July 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
653	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	682.00	-	10/2013 -	-	-	0/0
654	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	201.66	191.80	09/2008 -	09/2015	84(O) -	0/0
655	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	1,141.00	-	08/2013 -	-	-	0/0
656	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	1,509.10	-	09/2012 -	-	-	2/3
657	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	198.16	242.40	04/2008 12/2015	12/2015	92(O) 0(R)	0/0
658	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	175.96	-	04/2008 08/2015	08/2015	88(O) 0(R)	0/0
659	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	-	12/2009 -	-	-	0/0
660	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	361.00	-	02/2009 -	-	-	0/0
661	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	331.23	-	07/2009 -	-	-	0/0
662	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 -	212.00	-	09/2007 -	-	-	0/0
663	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	478.00	-	10/2013 -	-	-	0/0
664	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	625.07	995.90	01/2013 -	05/2015	-	0/0
665	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	946.00	737.50	- -	-	-	3/3
666	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	325.00	-	05/2013 -	-	-	0/0
667	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	-	04/2013 -	-	-	0/0
668	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	267.81	-	02/2013 -	-	-	0/0
669	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	792.06	-	12/2012 -	-	-	0/0
670	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	-	07/2013 -	-	-	0/0
671	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	-	01/2014 -	-	-	0/0
672	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	-	07/2013 -	-	-	0/0
673	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	795.00	-	05/2012 -	-	-	0/0
674	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	250.39	-	10/2008 -	-	-	0/0
675	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	-	07/2014 -	-	-	0/0
676	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,KARNATAKA	09/2010	671.00 -	671.00	1,273.00	- -	12/2015	-	2/3

Sector Wise Details									
(July 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
677	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90	635.90	-	07/2012	-	-	0/0
678	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04	280.13	173.80	11/2008	12/2015	85(O)	0/0
679	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81	385.13	-	04/2009	-	-	0/0
680	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64	167.64	-	11/2008	-	-	0/0
681	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00	200.00	-	04/2009	-	-	0/0
682	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00	1,267.00	-	06/2013	-	-	0/0
683	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00	754.00	-	03/2013	-	-	0/0
684	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72	264.72	-	06/2008	-	-	0/0
685	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19	484.19	285.50	10/2014	03/2016	17(O)	0/0
686	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00	208.00	-	04/2008	01/2016	93(O) 0(R)	0/0
687	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00	225.00	-	06/2008	08/2015	86(O) 0(R)	0/0
688	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00	200.00	281.60	06/2008	-	-	0/0
689	NASHRI-CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00	2,159.00	-	06/2015	-	-	0/0
690	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00	1,655.00	-	09/2013	-	-	0/0
691	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00	557.00	932.30	02/2010	-	-	0/0
692	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00	586.00	237.60	01/2014	12/2016	35(O)	0/0
693	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00	1,410.00	929.60	09/2014	06/2016	21(O)	0/0
694	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00	2,288.00	-	11/2011	-	-	0/0
695	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00	807.00	1,209.43	10/2014	10/2014	-	0/0
696	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69	942.69	-	06/2014	-	-	0/0
697	PATNA-BAKTARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00	574.00	-	03/2014	-	-	0/0
698	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30	671.30	-	02/2013	-	-	0/0
699	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00	940.00	-	07/2012	-	-	0/0
700	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55	1,724.55	-	03/2013	-	-	0/0
701	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00	835.00	-	01/2014	-	-	0/0

Sector Wise Details									
(July 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
702	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	-	07/2015 -	07/2015	0(O) -	0/0
703	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	251.03	326.30	10/2008 -	01/2015	-	0/0
704	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,MULTI STATE	12/2012	1,479.00 -	1,479.00	-	06/2015 -	06/2015	-	0/0
705	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN	03/2012	333.51 -	333.51	-	09/2014 -	-	-	0/0
706	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	650.00	-	11/2013 -	-	-	0/0
707	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	805.39	-	03/2013 -	-	-	0/0
708	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	909.00	982.90	05/2014 -	07/2015	14(O) -	0/0
709	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 - 157.47	154.57	228.30	09/2007 03/2014	03/2015	-	0/0
710	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	225.00	191.00	07/2008 -	-	-	0/0
711	SIX LANNING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	1,047.00	295.70	06/2014 -	03/2016	21(O) -	0/0
712	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	535.00	-	12/2013 -	-	-	0/0
713	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	-	12/2013 -	-	-	0/0
714	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	-	05/2014 -	-	-	0/0
715	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	-	08/2012 -	-	-	0/0
716	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	245.00	-	03/2008 01/2016	01/2016	94(O) 0(R)	0/0
717	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	-	06/2014 -	-	-	0/0
718	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	1,693.75	2,762.00	08/2011 -	09/2016	61(O) -	2/2
719	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	567.00	-	11/2013 -	-	-	0/0
720	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	-	10/2013 -	-	-	0/0
721	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	-	05/2013 -	-	-	0/0
722	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,KARNATAKA	11/2010	680.00 -	680.00	188.40	- -	07/2014	-	2/2
723	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,138.00	03/2014 -	04/2017	37(O) -	0/0
724	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI,ANDHRA PRADESH	09/2013	606.00 -	606.00	-	- -	-	-	0/0

Sector Wise Details									
(July 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
725	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	193.45	-	11/2012 -	-	-	0/0
726	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	1,287.95	-	11/2015 -	11/2015	0(O) -	0/0
727	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239]NHAI,RAJASTHAN	01/2014	368.15 -	368.15	27.32	01/2016 -	01/2016	0(O) -	0/0
728	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	-	02/2014 -	-	-	0/0
729	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI,TELANGANA	04/2014	1,123.17 -	1,123.17	-	-	-	-	0/0
	Total		100,051.30 -	101,875.35	19,064.80				14/28
	SHIPPING AND PORTS								
730	ACQUISITION OF TWO (2) NOS OF 317000 DWT VLCC'S FROM JIANGSU RONGSHENG HEAVY INDUSTRIES CO.LTD.,CHIN - [N25000064]SHIPP.,MAHARASHTRA	10/2010	994.82 -	402.24	427.54	11/2013 -	11/2013	-	0/0
731	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 -	1,460.00	1,049.37	12/2010 -	-	-	0/0
732	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 669.46	669.46	407.32	12/2010 -	01/2016	61(O) -	0/0
733	MODIFICATION AND STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST,GUJARAT	06/2010	277.00 -	277.00	0.21	03/2012 -	-	-	0/0
734	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 -	373.22	351.18	04/2009 -	-	-	0/0
735	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	2,427.40	831.23	10/2008 -	-	-	0/0
	Total		5,539.28 -	5,609.32	3,066.85				0/0
	TELECOMMUNICATIONS								
736	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	384.00	66.02	10/2010 08/2015	09/2015	59(O) 1(R)	0/0
737	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	13,334.00	-	07/2015 -	07/2015	0(O) -	0/0
	Total		13,718.00 -	13,718.00	66.02				0/0
	URBAN DEVELOPMENT								

Sector Wise Details									
(July 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
738	2000 BOYS HOSTEL (1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD, JHARKHAND	09/2012	171.86 -	171.86	-	03/2016 -	05/2016	2(O) -	0/0
739	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD, WEST BENGAL	01/2009	225.81 -	225.81	-	06/2012 -	05/2015	-	0/0
740	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP, KARNATAKA	05/2006	6,395.00 -	11,609.00	2,267.57	06/2011 -	-	-	3/3
741	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL, KARNATAKA	02/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019	0(O) -	0/0
742	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL, TAMIL NADU	02/2009	14,600.00 14,600.00	14,600.00	10,826.56	12/2015 -	08/2016	8(O) -	1/24
743	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD, DELHI	07/2012	884.30 -	884.30	-	08/2014 -	06/2017	34(O) -	0/0
744	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD, MADHYA PRADESH	12/2012	188.87 -	188.87	5.79	12/2014 -	12/2016	24(O) -	0/0
745	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD, DELHI	05/2009	261.85 -	261.85	6.26	05/2013 -	11/2015	30(O) -	0/0
746	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD, DELHI	05/2012	405.01 -	405.01	-	12/2014 -	04/2016	16(O) -	0/0
747	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD, ODISHA	11/2012	238.43 -	238.43	-	02/2015 -	08/2015	6(O) -	0/0
748	CONSTRUCTION OF MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB - [N28000070]CPWD, PUNJAB	08/2005	191.24 -	191.24	-	08/2007 -	03/2015	-	0/0
749	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD, KERALA	01/2010	165.23 -	165.23	-	10/2012 -	-	-	0/0
750	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD, MAHARASHTRA	12/2012	315.00 -	315.00	3.11	06/2015 -	08/2015	2(O) -	0/0
751	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD, WEST BENGAL	02/2014	156.57 -	156.57	-	09/2015 -	12/2016	15(O) -	0/0
752	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD, ANDHRA PRADESH	06/2014	157.84 -	157.84	-	03/2017 -	03/2017	0(O) -	0/0
753	DELHI MRTS PHASE-III - [N28000056]DMRCL, DELHI	09/2011	38,585.00 -	38,585.00	16,432.68	03/2016 -	12/2016	9(O) -	0/0
754	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA - [N28000078]CPWD, BIHAR	11/2006	2,727.89 -	2,727.89	-	03/2010 -	10/2014	-	0/0
755	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD, HIMACHAL PRADESH	11/2012	270.83 -	270.83	-	11/2014 -	10/2015	11(O) -	0/0

Sector Wise Details									
(July 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
756	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	1,219.21	-	07/2017 -	07/2017	0(0) -	0/0
757	FARIDABAD EXTENSION - [N28000057]DMRCL,DELHI	09/2011	2,494.00 -	2,494.00	1,272.44	09/2014 -	08/2015	11(0) -	0/0
758	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	5,181.79	-	07/2017 -	07/2017	0(0) -	0/0
759	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI - [N28000064]CPWD,DELHI	01/2010	162.90 -	162.90	-	07/2012 -	06/2014	-	0/0
760	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	12/2015	11(0) -	0/0
761	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	8,680.00	-	03/2018 -	03/2018	0(0) -	0/0
762	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 -	241.33	1.75	11/2014 -	12/2014	-	0/0
763	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI	06/2012	4,264.00 -	4,264.00	557.63	11/2019 -	11/2019	0(0) -	0/7
764	REHABILITATION AND STRENGTHENING OF SEWETRAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI(IN ZONE 2 IN - [N28000082]JnNURM,ANDHRA PRADESH	08/2007	246.90 -	246.90	-	-	-	-	0/0
765	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]CPWD,BIHAR	02/2012	171.10 -	171.10	-	09/2014 -	-	-	0/0
766	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	332.72	-	09/2016 -	09/2016	0(0) -	0/0
767	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	205.00	-	03/2012 -	04/2015	-	0/0
	Total		138,680.82 -	143,894.82	31,373.79				4/34
	Grand Total		1,055,580.91	1,262,000.07	499,450.58				1725/3774

* - Information in respect of Ministry of Railways is as on 01.01.2015. Ministry of Railways is not updating the information.

\$ - Time Overrun (Delay) = Anticipated Date of Commissioning minus Original Date of Commissioning.


Summary of projects in the Flash Report for the month of July, 2015

Project Implementation - Current Status:

Number of Projects in Previous Month	770
Number of Projects completed/dropped/frozen in Current Month	5
Number of Projects Added in Current Month	2
Number of Projects in Current Month	767


Brief Analysis

Project Status with respect to Original Schedule: Out of 767 projects, 7 projects are ahead of schedule, 125 projects are on schedule 233 projects are delayed. 373 projects do not have fixed dates of commissioning. 29 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

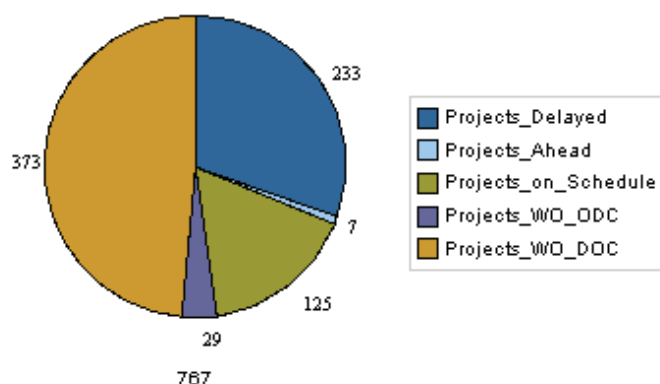

Investment Scenario

Total original cost of implementation of 767 projects when sanctioned, was of the order of Rs. 1055580.91 crore but this was subsequently revised to Rs. 1262000.07 crore implying a cost overrun of 19.6%. The expenditure incurred on these projects till July, 2015 is Rs. 499450.58 crore, which is 39.6% of the revised cost of the projects.

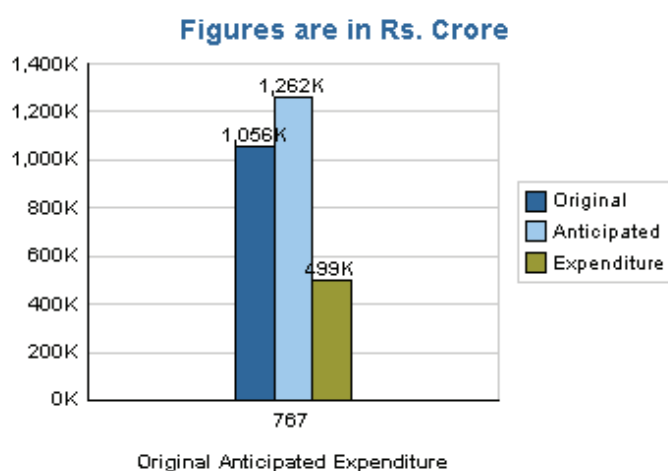

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	4


Brief Analysis

Project Status with respect to Original Schedule: All 4 projects are delayed.

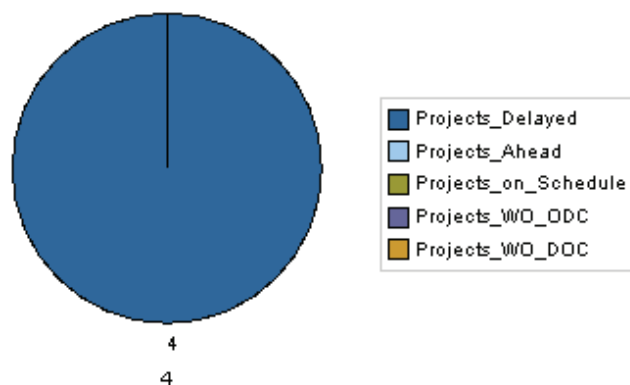

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 40442 crore but this was subsequently anticipated to Rs. 46726 crore implying a cost overrun of 15.5%. The expenditure incurred on these projects till July, 2015 is Rs. 37266.21 crore, which is 79.8% of the revised cost of the projects.

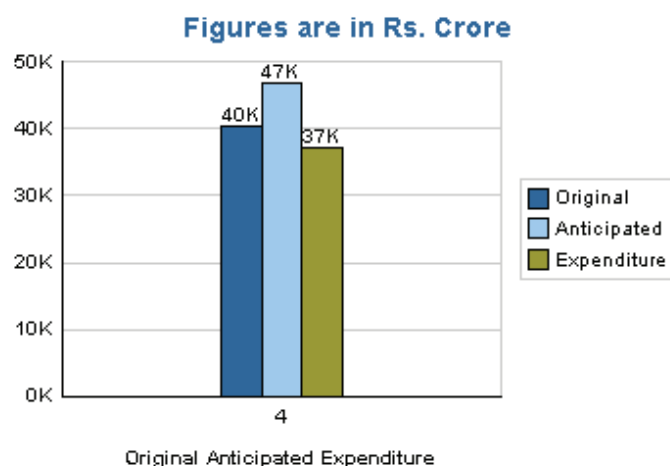

Sector wise current status of projects on the Flash Report


CIVIL AVIATION

Current Status:

Number of Projects	7
Number of Projects Delayed	3
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	3


Brief Analysis

Project Status with respect to Original Schedule: Out of 7 projects, 3 projects are delayed. 3 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

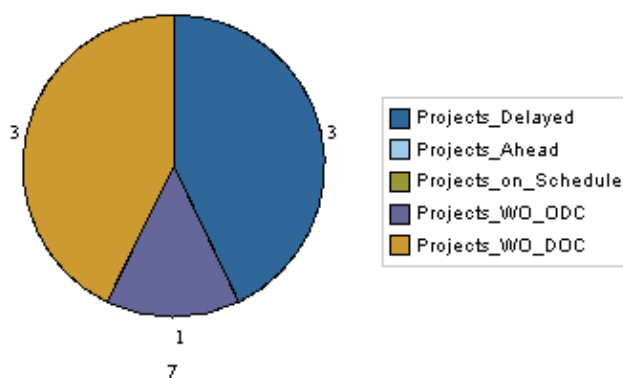

Investment Scenario

Total original cost of implementation of 7 projects when sanctioned, was of the order of Rs. 2599.56 crore but this was subsequently anticipated to Rs. 2645.45 crore implying a cost overrun of 1.8%. The expenditure incurred on these projects till July, 2015 is Rs. 1698.08 crore, which is 64.2% of the revised cost of the projects.

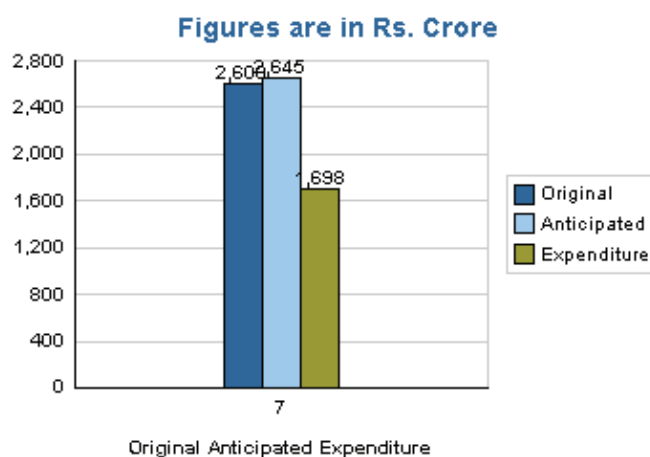

Sector wise current status of projects on the Flash Report


COAL

Current Status:

Number of Projects	77
Number of Projects On Schedule	30
Number of Projects Delayed	44
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	2


Brief Analysis

Project Status with respect to Original Schedule: Out of 77 projects, 1 project is ahead of schedule, 30 projects are on schedule 44 projects are delayed. 2 projects do not have fixed dates of commissioning.

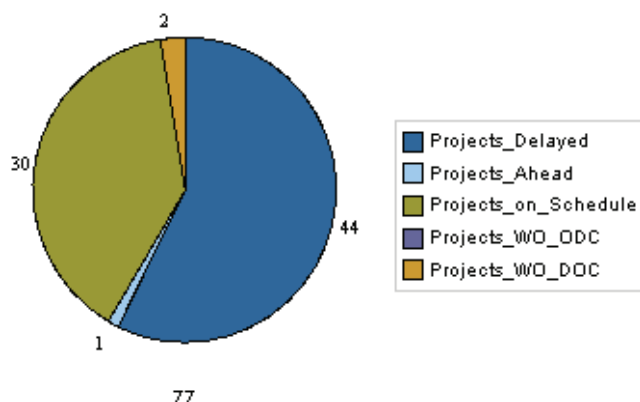

Investment Scenario

Total original cost of implementation of 77 projects when sanctioned, was of the order of Rs. 59875.1 crore but this was subsequently anticipated to Rs. 63778.26 crore implying a cost overrun of 6.5%. The expenditure incurred on these projects till July, 2015 is Rs. 22605.99 crore, which is 35.4% of the revised cost of the projects.

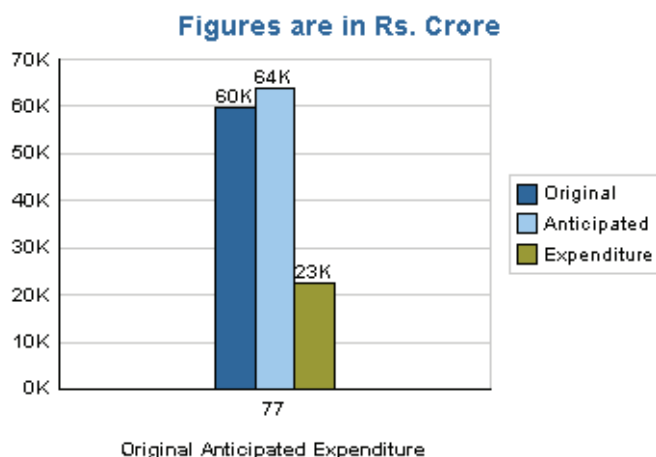

Sector wise current status of projects on the Flash Report

STEEL


Current Status:

Number of Projects	25
Number of Projects On Schedule	9
Number of Projects Delayed	12

Number of Projects Without Date Of Commissioning	4
--	---


Brief Analysis

Project Status with respect to Original Schedule: Out of 25 projects, 9 projects are on schedule 12 projects are delayed. 4 projects do not have fixed dates of commissioning.

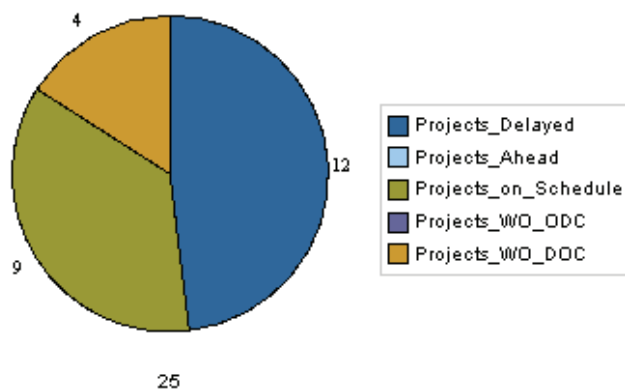

Investment Scenario

Total original cost of implementation of 25 projects when sanctioned, was of the order of Rs. 61386.16 crore but this was subsequently anticipated to Rs. 65130.56 crore implying a cost overrun of 6.1%. The expenditure incurred on these projects till July, 2015 is Rs. 42250.74 crore, which is 64.9% of the revised cost of the projects.

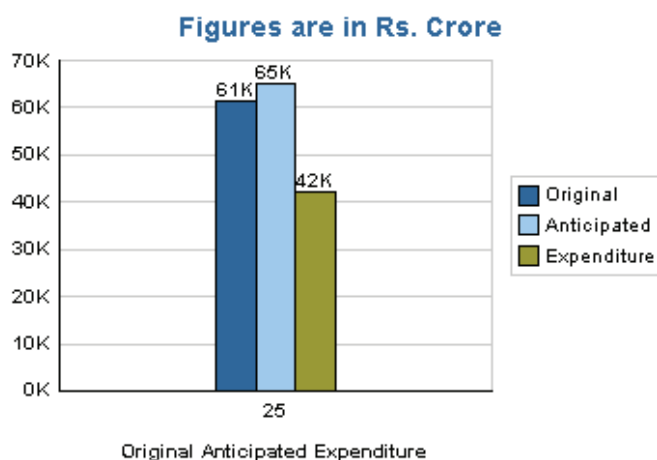

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	70
Number of Projects On Schedule	14
Number of Projects Delayed	42
Number of Projects Ahead	3
Number of Projects Without Date Of Commissioning	11


Brief Analysis

Project Status with respect to Original Schedule: Out of 70 projects, 3 projects are ahead of schedule, 14 projects are on schedule 42 projects are delayed. 11 projects do not have fixed dates of commissioning.

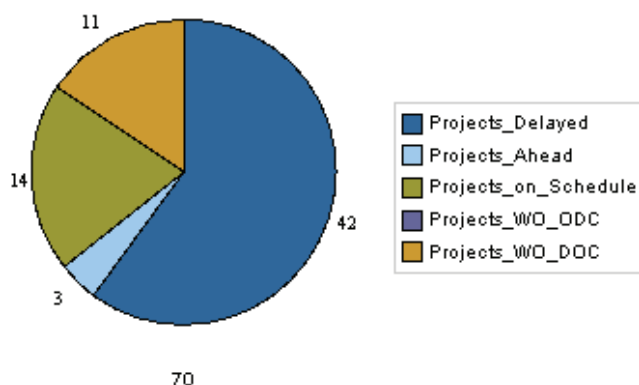

Investment Scenario

Total original cost of implementation of 70 projects when sanctioned, was of the order of Rs. 142903.11 crore but this was subsequently anticipated to Rs. 156858.71 crore implying a cost overrun of 9.8%. The expenditure incurred on these projects till July, 2015 is Rs. 72984.98 crore, which is 46.5% of the revised cost of the projects.

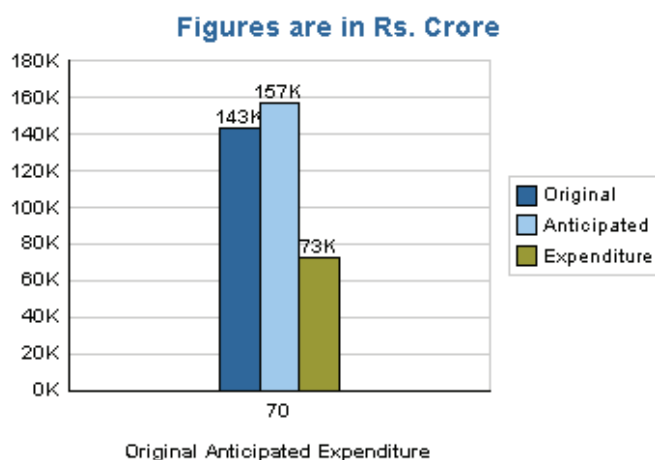

Sector wise current status of projects on the Flash Report


POWER

Current Status:

Number of Projects	109
Number of Projects On Schedule	42
Number of Projects Delayed	59
Number of Projects Ahead	3
Number of Projects Without Date Of Commissioning	5


Brief Analysis

Project Status with respect to Original Schedule: Out of 109 projects, 3 projects are ahead of schedule, 42 projects are on schedule 59 projects are delayed. 5 projects do not have fixed dates of commissioning.

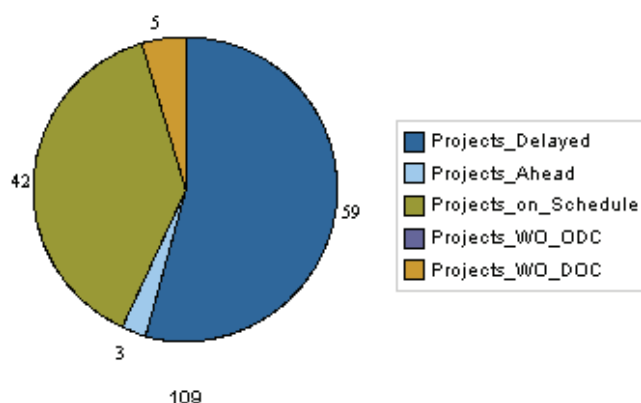

Investment Scenario

Total original cost of implementation of 109 projects when sanctioned, was of the order of Rs. 309271.77 crore but this was subsequently anticipated to Rs. 349101.15 crore implying a cost overrun of 12.9%. The expenditure incurred on these projects till July, 2015 is Rs. 172846.68 crore, which is 49.5% of the revised cost of the projects.

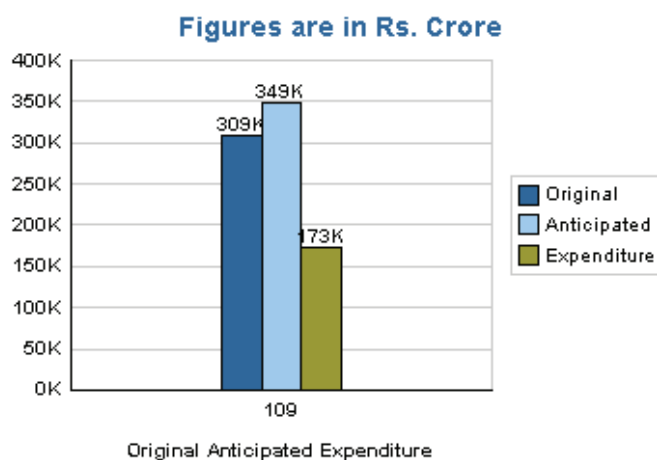

Sector wise current status of projects on the Flash Report


RAILWAYS

Current Status:

Number of Projects	296
Number of Projects On Schedule	8
Number of Projects Delayed	31
Number of Projects Without Original Date of Commissioning	27
Number of Projects Without Date Of Commissioning	230


Brief Analysis

Project Status with respect to Original Schedule: Out of 296 projects, 8 projects are on schedule 31 projects are delayed. 230 projects do not have fixed dates of commissioning. 27 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

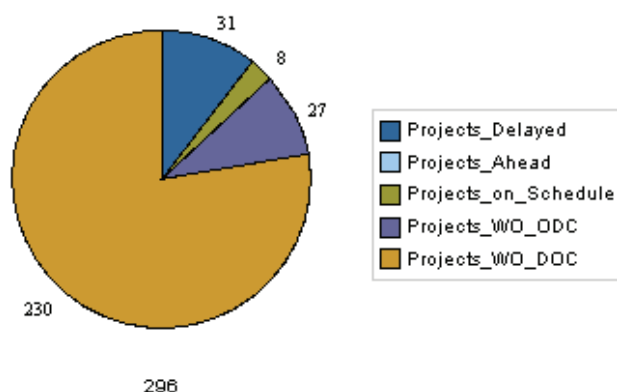

Investment Scenario

Total original cost of implementation of 296 projects when sanctioned, was of the order of Rs. 171881.41 crore but this was subsequently anticipated to Rs. 296947.84 crore implying a cost overrun of 72.8%. The expenditure incurred on these projects till July, 2015 is Rs. 87417.33 crore, which is 29.4% of the revised cost of the projects.

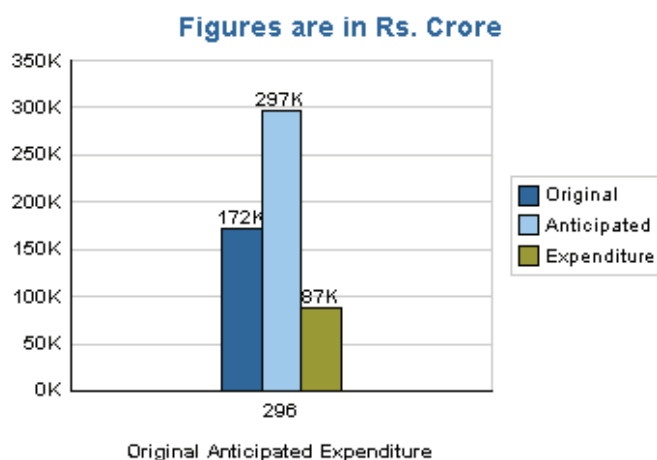

Sector wise current status of projects on the Flash Report


ROAD TRANSPORT AND HIGHW

Current Status:

Number of Projects	137
Number of Projects On Schedule	12
Number of Projects Delayed	21
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	103


Brief Analysis

Project Status with respect to Original Schedule: Out of 137 projects, 12 projects are on schedule 21 projects are delayed. 103 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

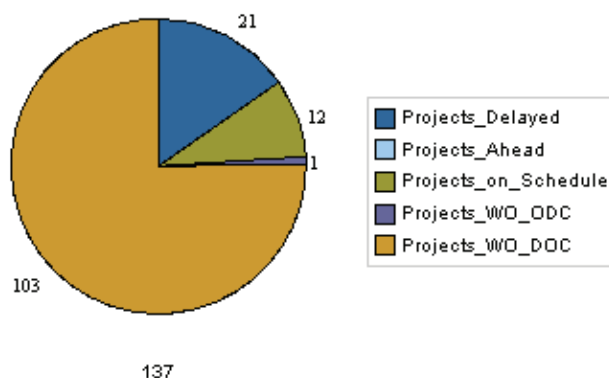

Investment Scenario

Total original cost of implementation of 137 projects when sanctioned, was of the order of Rs. 100051.3 crore but this was subsequently anticipated to Rs. 101875.35 crore implying a cost overrun of 1.8%. The expenditure incurred on these projects till July, 2015 is Rs. 19064.8 crore, which is 18.7% of the revised cost of the projects.

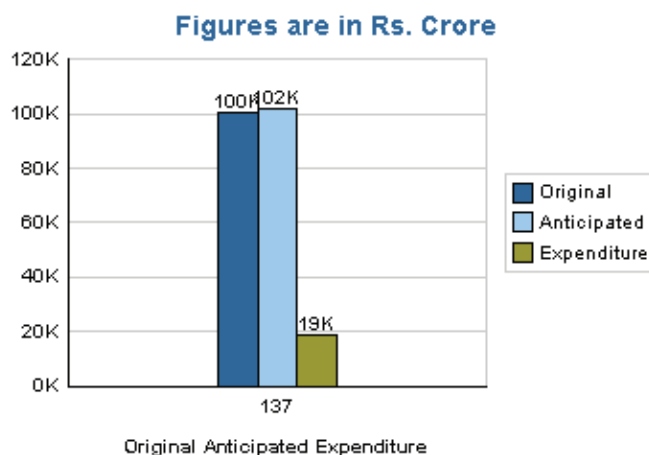

Sector wise current status of projects on the Flash Report


SHIPPING AND PORTS

Current Status:

Number of Projects	6
Number of Projects Delayed	1
Number of Projects Without Date Of Commissioning	5


Brief Analysis

Project Status with respect to Original Schedule: Out of 6 projects, 1 project is delayed. 5 projects do not have fixed dates of commissioning.

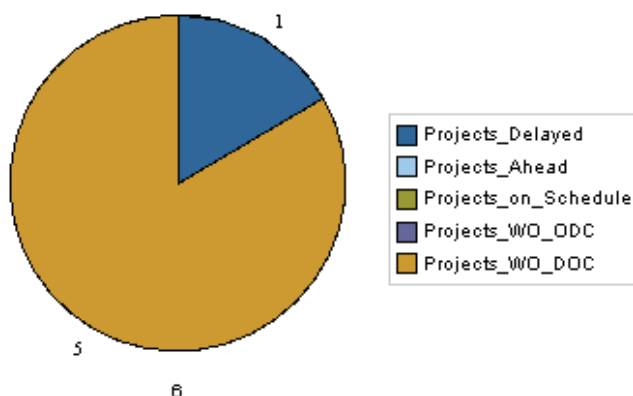

Investment Scenario

Total original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 5539.28 crore but this was subsequently anticipated to Rs. 5609.32 crore implying a cost overrun of 1.3%. The expenditure incurred on these projects till July, 2015 is Rs. 3066.85 crore, which is 54.7% of the revised cost of the projects.

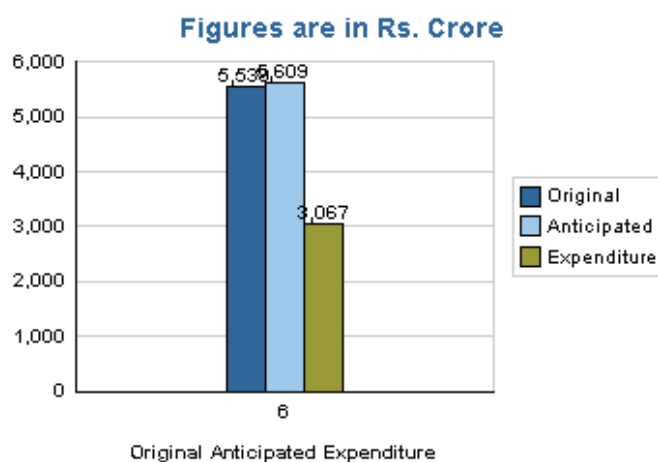

Sector wise current status of projects on the Flash Report


TELECOMMUNICATIONS

Current Status:

Number of Projects	2
Number of Projects On Schedule	1
Number of Projects Delayed	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 1 project is on schedule 1 project is delayed.

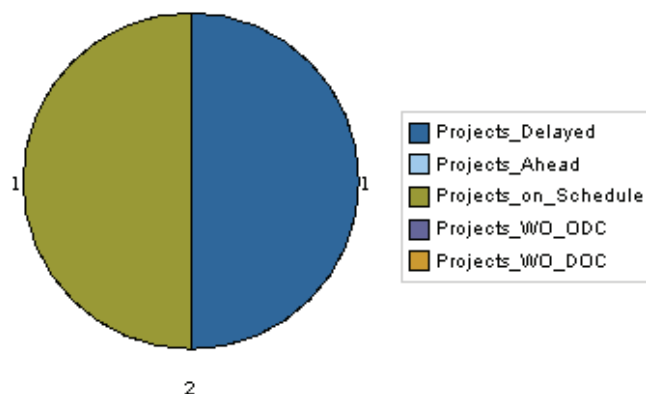

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 13718 crore but this was subsequently anticipated to Rs. 13718 crore. The expenditure incurred on these projects till July, 2015 is Rs. 66.02 crore, which is .5% of the revised cost of the projects.

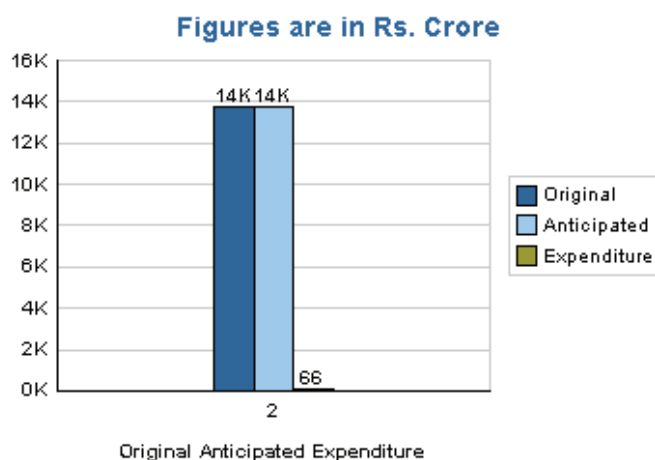

Sector wise current status of projects on the Flash Report


TELECOMMUNICATIONS

Current Status:

Number of Projects	2
Number of Projects On Schedule	1
Number of Projects Delayed	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 1 project is on schedule 1 project is delayed.

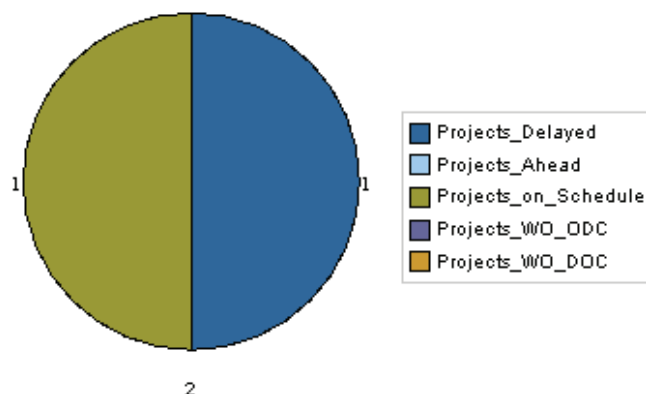

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 13718 crore but this was subsequently anticipated to Rs. 13718 crore. The expenditure incurred on these projects till July, 2015 is Rs. 66.02 crore, which is .5% of the revised cost of the projects.

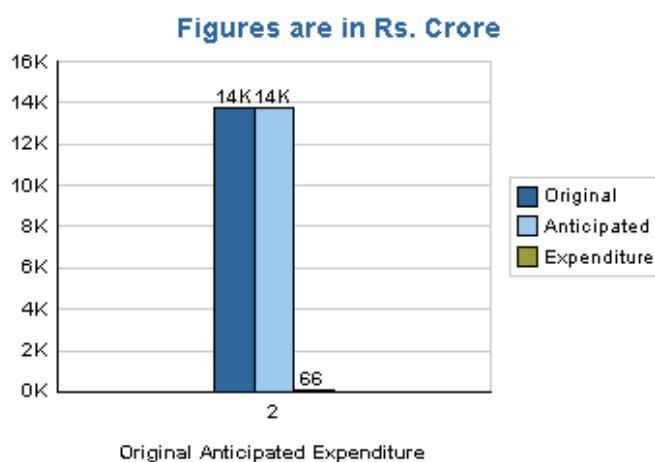

Sector wise current status of projects on the Flash Report

URBAN DEVELOPMENT


Current Status:

Number of Projects	30
Number of Projects On Schedule	7
Number of Projects Delayed	13

Number of Projects Without Date Of Commissioning	10
--	----


Brief Analysis

Project Status with respect to Original Schedule: Out of 30 projects, 7 projects are on schedule 13 projects are delayed. 10 projects do not have fixed dates of commissioning.

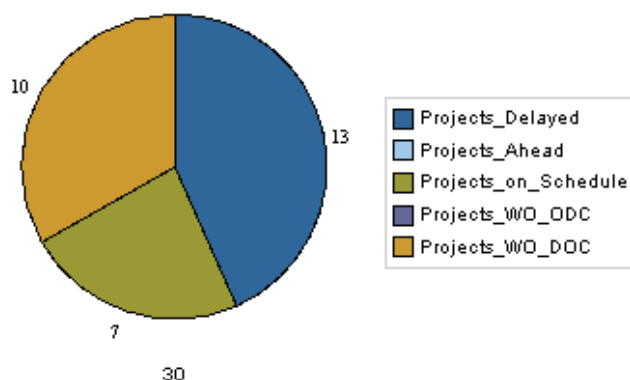

Investment Scenario

Total original cost of implementation of 30 projects when sanctioned, was of the order of Rs. 138680.82 crore but this was subsequently anticipated to Rs. 143894.82 crore implying a cost overrun of 3.8%. The expenditure incurred on these projects till July, 2015 is Rs. 31373.79 crore, which is 21.8% of the revised cost of the projects.

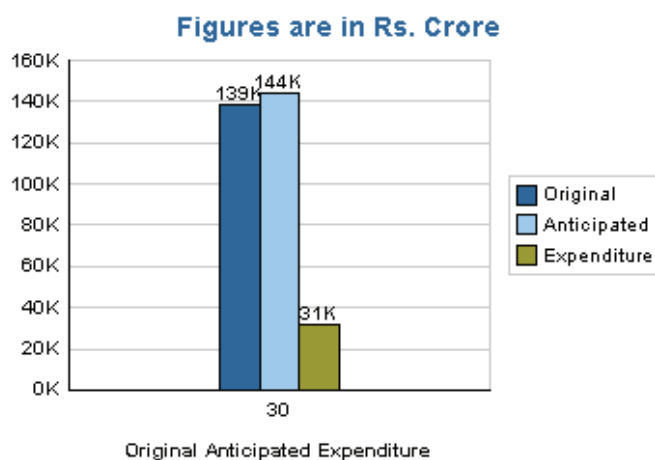

ANNEXURE

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE

(All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	ANDAMAN & NICOBAR ISLANDS	1	314.61	314.61	17.82
2	ANDHRA PRADESH	28	25,167.01	31,389.44	14,546.72
3	ARUNACHAL PRADESH	3	9,356.22	23,263.83	12,739.5
4	ASSAM	34	22,255.53	37,810.44	26,262.21
5	BIHAR	48	57,726.67	75,016.29	39,761.75
6	CHANDIGARH	1	452	489	468.24
7	CHHATISGARH	28	80,681.93	82,344.1	43,851.4
8	D & N HAVELI	1	6,086.08	6,086.08	84.54
9	DELHI	12	50,903.45	50,903.45	18,322.87
10	GOA	1	335.61	318	301.94
11	GUJARAT	28	35,207.34	35,994.98	13,373.76
12	HARYANA	9	4,659.81	6,630.43	1,852.6
13	HIMACHAL PRADESH	4	7,154.09	12,973.29	5,183.66
14	JAMMU AND KASHMIR	7	21,314.62	40,235.3	14,714.42
15	JHARKHAND	37	38,977.33	39,535.41	14,681.03
16	KARNATAKA	34	66,982.2	81,944.97	20,222.08
17	KERALA	13	24,457.67	28,611.45	10,169.06
18	MADHYA PRADESH	20	24,954.32	26,938.24	9,214.1
19	MAHARASHTRA	47	1,02,713.24	1,13,006.17	29,627.09
20	MANIPUR	1	727.56	6,570.75	2,787.99
21	MEGHALAYA	3	4,845.02	6,069.9	290.09
22	MIZORAM	2	988.06	4,201.96	1,057.25
23	MULTI STATE	184	1,95,719.93	2,24,032.39	75,361.89
24	NAGALAND	2	5,124	7,461.12	10.44
25	ODISHA	42	72,186.5	81,274.54	41,323.14
26	PUNJAB	3	792.5	765.46	190.47
27	RAJASTHAN	30	27,857.57	27,913.04	10,258.98
28	SIKKIM	2	1,648.94	4,499.46	445.91
29	TAMIL NADU	41	68,058.56	85,260.44	58,318.79
30	TELANGANA	22	9,807.71	12,632.35	2,986.56
31	TRIPURA	6	2,966.26	6,629.97	3,281.07
32	UTTAR PRADESH	29	35,842.78	38,623.19	9,123.12
33	UTTARAKHAND	6	9,351.89	12,905.21	4,692.4
34	WEST BENGAL	38	39,963.9	49,354.81	13,927.69
TOTAL		767	10,55,580.91	12,62,000.07	4,99,450.58

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
1	KUDANKULAM APP (NPCIL)	ATOMIC ENERGY	12/2001	13,171	17270	20,713
2	PARBATI HEP (4X200 MW) (NHPC) II	POWER	09/2002	3,919.59	-	5,142.86
3	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	POWER	09/2003	6,285.33	-	7,758.28
4	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	POWER	09/2005	1,061.38	-	1,813.21
5	VIRAMGAM-BHILDI (WR) , GC	RAILWAYS	04/1990	155.66	-	201.26
6	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL (SCR)	RAILWAYS	12/1994	124.43	-	712.02
7	UDHAMPUR-SRINAGAR-BARAMULLA (NL) , NR	RAILWAYS	03/1995	2,500	3000	10,658.34
8	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR (NL) , NEFR	RAILWAYS	04/1983	36.8	36.38	255.55
9	CALICUT-MANGALORE (DL) (SR)	RAILWAYS	02/1996	240	-	599.4
10	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA (NL) , SWR	RAILWAYS	02/1997	295	-	1,092.98
11	KARUR-SALEM (NL) , SR	RAILWAYS	02/1997	155.55	-	800.7
12	NANDYAL-YERRAGUNTALA (NL) , SCR	RAILWAYS	03/1996	155.74	164.36	755.5
13	KANPUR-KASGANJ-MATHURA (GC) , NER	RAILWAYS	03/1997	677.97	1062.36	1,621.4
14	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	RAILWAYS	09/1997	1,500	1000	3,410.06

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
15	MUNEERABAD-MAHABOBNAGAR (NL) , SCR	RAILWAYS	04/1997	218.24	236.41	309.19
16	RANCHI -LOHARDAGA (GC) , SER	RAILWAYS	04/1997	194.07	-	230.67
17	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	RAILWAYS	09/1998	247.66	-	488.76
18	JAYANAGAR-DARBHANGA-NARKATIA GANJ (GC) , ECR	RAILWAYS	04/1997	501.69	501.69	819.19
19	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	RAILWAYS	04/1999	108	427.21	436.85
20	KATI HAR - JOGBANI (GC) (NEFR)	RAILWAYS	09/2001	492.98	-	743.74
21	GULBARGA-BIDAR, SCR (NL)	RAILWAYS	02/1998	242.42	369.7	798.87
22	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD) , NR	RAILWAYS	03/2002	625.3	408.76	835.14
23	TIRUCHIRAPPALI-NAGORE-KARAIKKAL (SR) (GC)	RAILWAYS	09/1995	100	-	596.66
24	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR (SR) (GC)	RAILWAYS	03/1998	280	-	889.95
25	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) ,NEFR	RAILWAYS	04/2000	733	733	1,732.43
26	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT (MTP)	RAILWAYS	03/2000	1,049.69	3385.14	3,551.53
27	GADWAL - RAICHUR (NL) , SCR	RAILWAYS	04/1998	92.63	-	301.84
28	JIND-SONEPAT (NL) ,NR	RAILWAYS	01/2004	238.56	-	639.77

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
29	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	RAILWAYS	04/2003	727.56	727.56	2,787.99
30	KOSI BRIDGE (NL), ECR	RAILWAYS	04/2002	322.95	-	325.36
31	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR	RAILWAYS	04/2002	921	-	1,691.12
32	PATNA GANGA BRIDGE (NL), ECR	RAILWAYS	04/2001	624.47	-	2,521.72
33	ETAWAH-MAINPURI (NL), NCR	RAILWAYS	04/1997	120	245.39	249.33
34	CUTTACK - BARANG (LD)	RAILWAYS	04/1995	127.13	-	193.37
35	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	ROAD TRANSPORT AND HIGHWAYS	12/2003	157.47	157.47	228.3
36	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06	ROAD TRANSPORT AND HIGHWAYS	12/2003	155	-	191.8
37	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	ROAD TRANSPORT AND HIGHWAYS	12/2003	155.04	-	173.8
38	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	251.03	-	326.3
39	CONSTRUCTION OF NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT	CIVIL AVIATION	01/2009	309.46	-	357.35
40	MARKETING TOP AT KORBA	PETROLEUM	01/2011	141.86	-	147.6
41	KISHANGANGA HEP (3X110 MW)	POWER	01/2009	3,642.04	-	4,056.08
42	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	POWER	02/2010	2,144	-	2,176.1

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
43	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B	POWER	12/2010	2,743.19	-	2,783.3
44	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH	POWER	11/2011	2,127.51	-	2,211.93
45	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	RAILWAYS	04/1996	332.92	332.92	498.37
46	BHOPAL BINA 3D LINE DOUBLING	RAILWAYS	09/2007	687.2	-	793.71
47	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI	RAILWAYS	09/2007	404.19	-	457.88
48	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	RAILWAYS	09/2006	343.17	-	846.18
49	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	RAILWAYS	12/2006	170	-	417.7
50	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	RAILWAYS	09/2006	200	200	213.72
51	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	RAILWAYS	04/2006	325	-	420.71
52	AGARTALA SABROOM, NL, NEFR	RAILWAYS	04/2008	813.34	813.34	823.83
53	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	RAILWAYS	04/2007	482	-	730.11
54	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	RAILWAYS	04/1999	207.52	-	223.44
55	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	RAILWAYS	04/2006	117.36	196.95	198.83
56	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	RAILWAYS	04/1996	1,676.31	-	4,734.45

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
57	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR	RAILWAYS	04/2013	456	-	557.82
58	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	RAILWAYS	04/2010	739.65	-	794.11
59	SAKRI-HASANPUR ROAD (NL)	RAILWAYS	04/1999	175.69	-	258.31
60	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	RAILWAYS	04/1999	198.68	-	268.56
61	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	RAILWAYS	04/1998	271.24	-	462.69
62	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	RAILWAYS	04/2008	822.39	-	1,031.83
63	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	RAILWAYS	04/1999	895	575	1,005.81
64	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	RAILWAYS	04/2007	247	-	619.87
65	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI	RAILWAYS	04/1999	523.17	380.6	1,040.11
66	PEN ROHA DOUBLING	RAILWAYS	04/2007	98.74	-	227.84
67	PANVEL PEN DOUBLING	RAILWAYS	04/2006	96.16	-	240.21
68	MUNIRABAD (GINGERA) -RAICHUR NL	RAILWAYS	04/2007	179.65	-	380.62
69	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI	RAILWAYS	04/1999	460.94	-	800.9
70	JHARSUGUDA-RENGALI DOUBLING	RAILWAYS	03/2006	201	-	218.67

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
71	NALBARI TO BIJNI (AS-8)	ROAD TRANSPORT AND HIGHWAYS	12/2003	200	-	281.6
72	GUWAHATI TO NALBARI (AS-5)	ROAD TRANSPORT AND HIGHWAYS	12/2003	198.16	-	242.4
73	DHARAMTUL TO SONAPUR (AS-19)	ROAD TRANSPORT AND HIGHWAYS	12/2003	200	-	289.5
74	NH CONNECTIVITY TO ICTT VALLARPADAEU NH - SH	ROAD TRANSPORT AND HIGHWAYS	03/2005	557	-	932.3
75	SURAT- DAHISAR (SIX LANE) KM 263 TO KM 502	ROAD TRANSPORT AND HIGHWAYS	02/2009	1,693.75	-	2,762
76	HAZARIBAGH-RANCHI	ROAD TRANSPORT AND HIGHWAYS	08/2010	625.07	-	995.9
77	ARMUR TO KADLOOR YELLAREDDY	ROAD TRANSPORT AND HIGHWAYS	02/2010	390.56	-	631.7
78	KUNDUPUR-SURATHKAL & MANGLORE	ROAD TRANSPORT AND HIGHWAYS	09/2010	671	-	1,273
79	PANIPAT-ROHTAK	ROAD TRANSPORT AND HIGHWAYS	04/2011	807	-	1,209.43
80	2-LANNING OF SHILONG BYPASS	ROAD TRANSPORT AND HIGHWAYS	02/2011	226	-	282.3
81	SAMBALPUR-BARGARH- CHHATISGARH/ORISSA BORDER	ROAD TRANSPORT AND HIGHWAYS	11/2011	909	-	982.9
82	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	SHIPPING AND PORTS	03/2007	245.67	-	351.18

Details of Projects Ahead of Schedule w.r.t. Original Schedule

(July 2015)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>POWER</u>						
1	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154]	10/2013	1,315.90 -	1,315.90	508.77	10/2016 -	12/2015
	Total		1,315.90 -	1,315.90	508.77		
	<u>COAL</u>						
2	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	3.52	03/2021 -	03/2017
	Total		555.52 -	555.52	3.52		
	<u>PETROLEUM</u>						
3	MARKETING TOP AT KORBA - [N16000186]	1/2011	141.86 -	232.00	147.60	09/2016 -	12/2015
4	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]	7/2014	419.04 -	419.04	153.06	01/2017 -	06/2016
	Total		560.90 -	651.04	300.66		
	<u>POWER</u>						
5	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]	3/2015	1,071.24 -	1,071.24	-	10/2017 -	09/2017
	Total		1,071.24 -	1,071.24	.00		
	<u>PETROLEUM</u>						
6	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]	11/2014	6,068.80 -	6,068.80	401.81	04/2019 -	03/2019
	Total		6,068.80 -	6,068.80	401.81		
	<u>POWER</u>						
7	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I) - [N18000198]	5/2015	312.94 -	312.94	-	06/2016 -	05/2016
	Total		312.94 -	312.94	.00		
	Grand Total		9,885.30	9,975.44	1,214.76		

Details of On Schedule Projects w.r.t. Original Schedule

							(July 2015)
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
1	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
2	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	5/2015	397.09 -	397.09	-	03/2019 -	03/2019
3	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]	5/2014	479.15 -	479.15	-	03/2019 -	03/2019
4	GOKUL - [N06000120]	11/2014	267.67 -	267.67	152.29	03/2018 -	03/2018
5	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	107.24	03/2020 -	03/2020
6	AMERA OC RCE - [N06000123]	2/2015	335.97 -	335.97	29.73	03/2018 -	03/2018
7	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.10 -	490.10	203.68	03/2017 -	03/2017
8	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]	12/2009	510.85 -	510.85	223.15	03/2016 -	03/2016
9	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	11.77	03/2021 -	03/2021
10	KULDA EXPN OC. (5.00 MTY) - [N06000115]	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
11	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]	12/2009	1,352.04 -	1,143.54	804.28	03/2016 -	03/2016
12	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	295.56	59.83	03/2019 -	03/2019
13	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	114.82	03/2020 -	03/2020
14	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]	4/2012	258.56 -	258.56	84.31	03/2016 -	03/2016
15	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	486.27	71.01	03/2016 -	03/2016
16	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	764.69	03/2023 03/2023	03/2023
17	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	5.43	03/2023 03/2023	03/2023
18	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]	5/2014	337.66 -	337.66	-	03/2019 -	03/2019
19	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	6.08	03/2020 -	03/2020
20	KAPURIA UG(PSLW) - [N06000108]	8/2011	988.35 -	988.35	45.15	04/2017 04/2017	04/2017
21	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	81.08	03/2021 -	03/2021
22	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]	8/2012	1,055.05 -	1,055.05	156.87	03/2018 -	03/2018

							(July 2015)
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
23	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	111.96	03/2016 -	03/2016
24	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	26.37	03/2021 -	03/2021
25	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	0.56	03/2026 -	03/2026
26	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	76.43	03/2020 -	03/2020
27	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	92.65	03/2018 -	03/2018
28	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.33	-	03/2022 -	03/2022
29	BHANEAGAON OC - [N06000121]	2/2015	187.94 -	187.94	40.78	03/2023 -	03/2023
30	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	108.44	03/2021 -	03/2021
	Total		27,488.88 -	27,383.90	3,378.60		
	<u>FERTILISERS</u>						
31	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	197.79	24.66	11/2016 -	11/2016
	Total		197.79 -	197.79	24.66		
	<u>MINES</u>						
32	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]	9/2011	1,856.00 -	1,856.00	-	09/2017 -	09/2017
	Total		1,856.00 -	1,856.00	.00		
	<u>PETROLEUM</u>						
33	REWARI KANPUR PIPELINE PROJECT - [N16000145]	2/2012	1,210.64 -	1,446.34	1,066.43	11/2015 -	11/2015
34	TWENTY NOS. FEEDER GAS LINES - [N16000192]	3/2009	228.64 -	214.19	130.94	12/2016 -	12/2016
35	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]	3/2014	2,476.82 -	2,476.82	149.73	12/2018 -	12/2018
36	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	6/2014	5,706.47 -	5,813.25	1,553.25	05/2017 05/2017	05/2017
37	PARADIP LPG IMPORT FACILITY - [N16000196]	1/2015	690.00 -	690.00	-	07/2018 -	07/2018
38	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	7/2011	352.56 -	450.55	10.60	03/2017 -	03/2017
39	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]	3/2014	238.50 -	238.50	1.07	03/2017 -	03/2017
40	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00 -	3,150.00	108.21	09/2017 -	09/2017

(July 2015)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
41	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]	12/2011	160.00 -	160.00	2.47	02/2016 02/2016	02/2016
42	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]	2/2014	163.88 -	163.88	25.70	07/2016 -	07/2016
43	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]	5/2015	257.87 -	257.87	5.37	11/2016 -	11/2016
44	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]	9/2011	202.25 -	160.16	60.63	07/2016 -	07/2016
45	CRU TO ISOMERIZATION (ISOM) - [N16000200]	10/2011	725.00 -	725.00	23.91	11/2016 -	11/2016
46	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	3/2012	14,225.00 -	16,504.00	7,147.44	05/2016 -	05/2016
	Total		29,787.63 -	32,450.56	10,285.75		
	POWER						
47	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	141.00	08/2017 -	08/2017
48	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	12,532.44	1,713.00	08/2018 -	08/2018
49	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	1/2015	203.28 -	203.28	0.20	07/2017 -	07/2017
50	NPCCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	1/2013	12,964.60 -	12,964.60	3,767.88	01/2018 -	01/2018
51	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]	5/2015	780.33 -	780.33	-	07/2017 -	07/2017
52	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	488.30	03/2018 -	03/2018
53	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]	3/2015	550.06 -	550.06	1.60	03/2018 -	03/2018
54	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	717.00	03/2019 -	03/2019
55	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]	2/2014	378.71 -	378.71	81.90	10/2016 -	10/2016
56	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]	1/2015	268.80 -	268.80	0.80	03/2018 -	03/2018
57	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	11,638.55	3,675.00	09/2017 -	09/2017
58	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.84	119.00	09/2019 -	09/2019
59	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]	5/2014	303.07 -	303.07	2.30	07/2016 -	07/2016
60	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]	2/2014	539.82 -	539.82	62.50	06/2016 -	06/2016
61	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]	10/2014	8,112.12 -	8,112.12	-	04/2020 -	04/2020
62	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]	4/2015	1,479.30 -	1,479.30	31.40	04/2017 -	04/2017

(July 2015)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
63	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]	3/2015	1,394.52	1,394.52	-	05/2017	05/2017
64	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]	3/2014	155.57	155.57	1.00	05/2016	05/2016
65	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29	522.29	30.00	11/2016	11/2016
66	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]	9/2013	1,575.30	1,575.30	370.20	05/2016	05/2016
67	WARDHA-HYDERABAD 765 KV LINK - [N18000183]	1/2015	3,662.02	3,662.02	62.90	05/2018	05/2018
68	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	2/2014	908.08	908.08	53.70	06/2016	06/2016
69	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	2/2014	196.58	196.58	1.00	02/2016	02/2016
70	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]	11/2014	972.42	972.42	-	11/2017	11/2017
71	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]	2/2014	243.53	243.53	146.50	08/2016	08/2016
72	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]	2/2014	167.40	167.40	68.80	12/2015	12/2015
73	KUDGI STPP STAGE 1 - [N18000131]	1/2012	15,166.19	15,166.19	8,655.00	01/2017	01/2017
74	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]	8/2014	288.49	288.49	23.40	02/2017	02/2017
75	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]	9/2013	680.69	680.69	298.89	03/2016	03/2016
76	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58	14,366.58	2,140.00	02/2019	02/2019
77	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]	5/2014	829.98	829.98	2.00	08/2016	08/2016
78	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]	1/2015	871.62	871.62	1.90	11/2017	11/2017
79	VINDHYACHAL STPP STAGE-V - [N18000134]	5/2012	3,180.40	3,180.40	1,981.00	08/2015	08/2015
80	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]	6/2014	400.47	400.47	10.40	04/2017	04/2017
81	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]	8/2014	188.75	188.75	1.00	02/2017	02/2017
82	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52	1,364.52	278.34	04/2016	04/2016
83	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00	11,846.00	4,529.00	06/2017	06/2017
84	MOUDA STPP STAGE 2 - [N18000132]	3/2012	7,921.47	7,921.47	4,309.00	09/2016	09/2016
85	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]	12/2014	6,517.36	6,517.36	111.80	04/2018	04/2018
86	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]	4/2015	3,705.61	3,705.61	57.40	04/2018	04/2018

							(July 2015)	
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	
1	2	3	4	5	6	7	8	
87	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184	3/2015	197.40 -	197.40	-	04/2018 -	04/2018	
88	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174	7/2013	3,363.12 -	3,363.12	698.00	12/2016 -	12/2016	
	Total		147,686.63 -	147,686.63	34,633.11			
	<u>RAILWAYS</u>							
89	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR & TAMPUR-BANSI PAHARPUR - [N22000158	4/2010	622.41 -	2,030.50	3.61	02/2019 -	02/2019	
90	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	4/2012	148.77 -	209.00	2.64	12/2016 -	12/2016	
91	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245	4/2010	423.66 -	423.66	163.59	03/2017 -	03/2017	
92	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213	4/2012	632.68 -	816.55	-	03/2016 -	03/2016	
93	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	4/2011	1,176.09 -	3,845.60	2.33	02/2020 -	02/2020	
94	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239	4/2011	299.60 -	299.60	1.10	03/2017 -	03/2017	
95	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111	4/2010	2,913.51 -	2,619.02	-	03/2016 -	03/2016	
96	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110	4/2010	3,951.98 -	3,951.98	-	03/2016 -	03/2016	
	Total		10,168.70 -	14,195.91	173.27			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
97	2-LANING WITH PS OF JHALAWAR-RAJASTHAN-MP. BORDER - [N24000237	1/2014	177.32 -	177.32	86.65	01/2016 -	01/2016	
98	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240	3/2014	240.10 -	240.10	-	03/2016 -	03/2016	
99	AHMEDABAD TO VADODARA SECTION - [N24000222	1/2013	2,125.24 -	2,125.24	163.30	12/2015 -	12/2015	
100	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236	10/2013	677.79 -	677.79	59.09	04/2016 -	04/2016	
101	ETAWAH CHAKERI - [N24000219	3/2013	1,573.00 -	1,573.00	-	09/2015 -	09/2015	
102	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233	4/2014	1,266.60 -	1,266.60	-	09/2016 -	09/2016	
103	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR - [N24000238	1/2014	158.04 -	158.04	2.67	12/2015 -	12/2015	
104	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161	7/2010	1,987.00 -	1,987.00	-	07/2015 -	07/2015	
105	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228	6/2013	1,287.95 -	1,287.95	-	11/2015 -	11/2015	

							(July 2015)
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
106	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239]	1/2014	368.15 -	368.15	27.32	01/2016 -	01/2016
107	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]	11/2013	1,916.79 -	1,916.79	-	11/2016 -	11/2016
108	4-LANING OF ROHATAK JIND (LENGTH 45 KM) - [N24000231]	10/2013	283.25 -	283.25	-	10/2015 -	10/2015
	Total		12,061.23 -	12,061.23	339.03		
	<u>STEEL</u>						
109	REBUILDING OF COB-7 AT BSL - [N12000083]	10/2013	245.67 -	245.67	51.94	05/2016 -	05/2016
110	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]	5/2015	1,154.18 -	1,154.18	-	12/2017 -	12/2017
111	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]	6/2014	708.91 -	708.91	159.27	04/2016 -	04/2016
112	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	25.49	10/2016 -	10/2016
113	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]	3/2015	1,034.01 -	1,034.01	-	10/2017 -	10/2017
114	TURBO BLOWER - 5 - [N12000092]	12/2009	280.00 -	280.00	13.77	09/2016 -	09/2016
115	3RD CONVERTER AND 4TH CASTER - [N12000088]	7/2011	974.76 -	974.76	147.85	07/2016 -	07/2016
116	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]	4/2015	3,127.30 -	3,127.30	5.18	04/2018 -	04/2018
117	ALTERNATE GAS NETWORK AT BSL - [N12000093]	3/2015	255.19 -	255.19	-	03/2018 -	03/2018
	Total		8,123.02 -	8,268.42	403.50		
	<u>TELECOMMUNICATIONS</u>						
118	NETWORK FOR SPECTRUM - [N26000101]	3/2012	13,334.00 -	13,334.00	-	07/2015 -	07/2015
	Total		13,334.00 -	13,334.00	.00		
	<u>URBAN DEVELOPMENT</u>						
119	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]	2/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019
120	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]	4/2014	332.72 -	332.72	-	09/2016 -	09/2016
121	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]	6/2014	157.84 -	157.84	-	03/2017 -	03/2017
122	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,219.21	-	07/2017 -	07/2017
123	NAGPUR METRO RAIL - [N28000085]	8/2014	8,680.00 -	8,680.00	-	03/2018 -	03/2018

(July 2015)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
124	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080	6/2012	4,264.00 -	4,264.00	557.63	11/2019 -	11/2019
125	KOCHI METRO RAIL PROJECT - [N28000081	7/2012	5,181.79 -	5,181.79	-	07/2017 -	07/2017
	Total		46,240.70 -	46,240.70	557.63		
	Grand Total		296,944.58	303,675.14	49,795.55		

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(July 2015)

S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs crore)	Anticipated Cost (Rs.crore)	Date of Commissioning (Month/Year)		Cost Overruns (%)
					Original/ Revised	Anticipated	
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	09/2016	62.57
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	12/2008 -	10/2015	31.12
	Total		16,663.00 -	22,947.00			
	<u>CIVIL AVIATION</u>						
3	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT (MOHALI) PH - II - [N04000070]	02/2011	452.00 -	489.00	03/2015 -	07/2015	8.19
4	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]	10/2012	217.60 -	244.10	03/2015 -	09/2015	12.18
	Total		669.60 -	733.10			
	<u>COAL</u>						
5	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	03/2016 -	03/2016	31.87
6	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,583.77	06/2009 -	07/2015	76.47
7	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	03/2016	478.50
8	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	479.63	03/2013 -	03/2017	0.02
9	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,602.74	03/2012 -	08/2015	34.63
10	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	486.27	03/2016 -	03/2016	12.97
	Total		8,208.23 -	12,579.39			
	<u>HEAVY INDUSTRY</u>						
11	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78
	Total		1,718.00 -	3,827.30			

(July 2015)

(July 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>PETROCHEMICALS</u>						
12	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	9,833.52	04/2012 -	09/2015	80.08
	Total		5,460.61 -	9,833.52			
	<u>PETROLEUM</u>						
13	DEVELOPMENT OF G1 AND GS-15 (ONGCL) - [160100231]	04/2003	429.82 -	3,955.21	04/2006 -	06/2015	820.20
14	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]	12/2012	3,513.07 -	4,619.94	02/2016 -	12/2017	31.51
15	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	450.55	03/2017 -	03/2017	27.79
16	MARKETING TERMINAL AT PARADEEP - [N16000168]	07/2009	199.75 -	239.73	07/2013 -	10/2015	20.02
17	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	01/2016	70.49
18	MARKETING TOP AT KORBA - [N16000186]	01/2011	141.86 -	232.00	09/2016 -	12/2015	63.54
19	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	06/2014	5,706.47 -	5,813.25	05/2017 -	05/2017	1.87
20	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79 -	1,256.72	05/2013 -	12/2015	45.83
21	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00 -	34,555.00	11/2012 -	10/2015	16.05
22	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	05/2016	29.42
23	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	03/2012	14,225.00 -	16,504.00	05/2016 -	05/2016	16.02
24	REWARI KANPUR PIPELINE PROJECT - [N16000145]	02/2012	1,210.64 -	1,446.34	11/2015 -	11/2015	19.47
25	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	02/2012	666.00 -	838.08	11/2015 -	11/2016	25.84
26	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79	10/2014 -	10/2016	49.38
27	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]	01/2006	672.00 -	1,178.35	10/2011 -	06/2015	75.35
28	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]	01/2006	732.00 -	1,227.00	10/2011 -	01/2016	67.62
29	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	06/2016	37.72
	Total		62,721.75 -	78,337.61			

(July 2015)

(July 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>POWER</u>						
30	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	7,818.68	09/2009 -	12/2018	99.48
31	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	15,300.00	09/2010 -	-	143.42
32	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]	09/2005	1,061.38 -	1,929.15	09/2009 -	06/2016	81.76
33	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	721.81	09/2010 -	03/2016	51.10
34	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]	03/2011	2,569.25 -	3,105.51	03/2014 -	08/2015	20.87
35	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]	09/2010	2,074.86 -	2,348.37	03/2013 -	10/2015	13.18
36	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]	07/2012	296.87 -	363.73	12/2014 -	05/2015	22.52
37	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	12/2018	29.14
38	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	6,749.18	09/2011 -	03/2017	54.25
39	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,745.08	06/2013 -	12/2019	50.31
40	BARH STPP STAGE -II - [N18000047]	02/2008	7,341.04 -	10,852.46	10/2013 -	03/2015	47.83
41	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,476.34	12/2009 06/2016	03/2017	159.38
42	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	07/2010 -	05/2018	79.77
43	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,487.49	08/2013 -	03/2016	159.15
44	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	346.79	08/2014 -	12/2015	16.63
45	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]	12/2011	1,746.65 -	2,228.71	08/2014 -	03/2016	27.60
46	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,497.72	01/2016 -	11/2016	50.95
47	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,159.07	09/2008 -	03/2016	21.34
48	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	15,095.67	01/2011 -	03/2018	73.65
49	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	07/1998	368.72 -	1,381.71	07/2006 02/2015	10/2016	274.73
50	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	1,007.68	07/2013 -	08/2015	139.35
	Total		55,547.32 -	95,440.31			

(July 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>RAILWAYS</u>						
51	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007	04/1986	158.77 274.56	608.02	03/1994 -	03/2015	282.96
52	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135	04/1983	36.80 274.41	1,336.57	- -	03/2019	3,531.98
53	CALICUT-MANGALORE (DL) (SR) - [220100151	02/1996	240.00 -	579.37	- -	02/2012	141.40
54	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	800.00	- -	-	414.30
55	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	492.98 -	1,727.27	12/2010 -	03/2018	250.37
56	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	844.00	- 05/2009	03/2015	248.16
57	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263	03/1998	280.00 -	1,122.00	- -	-	300.71
58	KOTLALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	330.00 -	1,047.00	- -	-	217.27
59	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
60	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	02/2011 -	-	191.48
61	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	2,371.85	03/2005 12/2008	12/2019	2,019.62
62	JIND-SONEPAT (NL),NR - [220100280	01/2004	238.56 -	740.00	03/2012 -	12/2012	210.19
63	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06
64	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	03/2009 -	10/2015	156.57
65	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314	04/2001	470.92 727.13	1,225.90	- -	03/2017	160.32
66	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316	04/2003	218.19 -	343.00	- -	-	57.20
67	ETAWAH-MAINPURI (NL),NCR - [220100318	04/1997	120.00 -	245.39	12/2008 -	10/2015	104.49
68	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	1,101.16	- -	03/2017	186.92
69	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	818.29	02/2015 -	-	346.59
70	CUTTACK - BARANG (LD) - [220100326	04/1995	127.13 -	225.00	- -	10/2014	76.98
71	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	276.00	03/2009 03/2009	08/2014	106.88
72	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	810.78 -	810.80	- -	-	0.00

(July 2015)

(July 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
73	RAICHUR-GUNTAKAL(DL)(SCR) - [N20100329]	04/2003	136.62 -	289.93	12/2007 03/2010	-	112.22
74	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1997	261.70 -	280.00	02/2006 -	-	6.99
75	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41
76	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI [N22000079]	09/2007	404.19 -	1,383.45	- -	-	242.28
77	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE [N22000080]	09/2006	343.17 -	914.98	- -	03/2016	166.63
78	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 -	490.00	- -	-	292.00
79	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	1,080.00	- -	-	136.84
80	ELECTRIFICATION OF KHURJA-MEERUT- SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	03/2016	60.77
81	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,820.25	04/2014 -	03/2018	355.36
82	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	332.92 283.95	477.88	03/2012 -	-	43.54
83	VIRAMGAM-BHILDI(WR),GC - [220100062]	04/1990	155.66 -	548.01	- 03/2010	-	252.06
84	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56 -	791.59	- -	-	109.11
85	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 -	1,117.11	03/2008 06/2008	-	50.35
86	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) [N22000113]	04/2008	653.19 -	653.55	03/2014 -	-	0.06
87	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012 -	-	135.68
88	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]	04/2006	117.36 196.95	196.95	03/2011 -	-	67.82
89	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41
90	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	499.30 -	2,501.05	- -	-	400.91
91	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70 -	279.70	- -	-	0.72
92	PEN ROHA DOUBLING - [N22000254]	04/2007	98.74 -	203.00	- -	03/2015	105.59
93	PANVEL PEN DOUBLING - [N22000255]	04/2006	96.16 -	260.16	- -	01/2015	170.55
94	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26

(July 2015)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
95	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	-	651.97
96	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97
97	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]	04/2008	184.26 -	2,000.00	- -	-	985.42
98	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	576.18	- -	-	100.76
99	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99	- -	-	183.41
100	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL [N22000276]	04/2013	558.00 -	692.43	- -	-	24.09
101	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	-	57.65
102	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	- -	-	47.93
103	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,743.00	- -	-	79.63
104	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29
105	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	337.50	- -	-	0.00
106	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	329.97	- -	-	50.10
107	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	-	14.14
108	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00	- -	-	72.07
109	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	-	12.38
110	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]	04/1999	460.94 -	1,030.00	01/1999 -	-	123.46
111	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	800.00	01/1999 -	-	71.50
112	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	01/1999 -	-	53.96
113	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181]	02/1997	514.68 -	2,820.00	- -	-	447.91
114	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	1,781.98	03/2004 -	03/2016	259.68
115	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	06/2017	233.08
116	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	1,630.97	05/2008 -	-	558.55
117	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	04/1997	501.69 335.77	1,043.56	03/2012 -	-	108.01
118	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	12/2009 -	06/2015	300.67

(July 2015)

(July 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
119	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257	04/1997	162.87 -	541.00	- -	-	232.17
120	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	2,531.34	12/2008 -	03/2018	245.34
121	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	470.21 -	1,995.25	- -	-	324.33
122	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	6,570.75	03/2011 -	03/2019	803.12
123	KOSI BRIDGE (NL), ECR - [220100304	04/2002	322.95 -	341.41	03/2012 -	-	5.72
124	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76
125	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082	12/2006	170.00 -	485.00	03/2011 -	-	185.29
126	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR [N22000086	09/2006	200.00 -	496.24	- -	03/2017	148.12
127	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087	09/2006	300.00 -	827.73	- -	03/2019	175.91
128	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124	04/2006	850.00 -	2,973.42	03/2015 -	03/2020	249.81
129	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
130	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127	04/1996	1,676.31 -	5,500.00	03/2009 -	03/2016	228.10
131	AGARTALA SABROOM, NL, NEFR - [N22000099	04/2008	813.34 -	2,876.00	03/2014 -	03/2018	253.60
132	KISHANGANJ JALALGARH, NL, NEFR - [N22000101	04/2008	282.92 -	565.13	- -	03/2018	99.75
133	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	4,190.00	12/2015 -	03/2020	212.81
134	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197	03/1997	677.97 1,062.36	1,651.54	- -	03/2018	143.60
135	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
136	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60
137	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	625.30 408.76	847.75	06/2007 -	-	35.57
138	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	04/2006	325.00 -	1,564.54	03/2010 -	03/2017	381.40
139	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	968.60	12/2012 -	-	218.62
140	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	288.00	02/2009 02/2009	08/2014	73.33

(July 2015)

(July 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
141	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075	09/2006	324.90 -	385.54	03/2010 -	-	18.66
142	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192	03/1996	155.74 164.36	883.00	02/2009 -	03/2015	466.97
143	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	645.00	- -	03/2015	195.55
144	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
145	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,544.40	03/1998 -	12/2019	299.79
146	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	03/2015	160.76
147	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097	03/1984	293.97 -	1,428.00	06/2005 -	12/2019	385.76
148	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	335.00	06/2004 -	12/2015	72.62
149	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	- -	-	840.53
150	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR [220100183	02/1997	295.00 -	1,289.92	- -	-	337.26
151	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	04/1996	138.00 -	1,382.78	- -	-	902.01
152	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107	04/2007	482.00 -	874.57	03/2013 -	09/2015	81.45
153	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	980.00	- -	-	880.00
154	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) [N22000123	04/2008	318.24 -	321.62	03/2012 -	-	1.06
155	SAMBALPUR-TALCHER DOUBLING - [N22000315	03/2011	679.27 -	1,111.99	- -	-	63.70
156	JHARSUGUDA-RENGALI DOUBLING - [N22000317	03/2006	201.00 -	230.00	- -	-	14.43
157	KIRANDUL - JAGDALPUR DOUBLING - [N22000318	12/2012	826.57 -	1,143.60	- -	03/2018	38.35
158	DELANG-PURI DOUBLING - [N22000320	03/2011	165.16 -	234.71	03/2015 -	03/2015	42.11
159	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321	04/2014	182.92 -	197.73	- -	-	8.10
160	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND [N22000323	04/2012	148.77 -	209.00	12/2016 -	12/2016	40.49
161	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	925.30	- -	02/2014	643.63
162	AMRAVATI-NARKHER NL(CR) - [220100118	06/1994	663.01 175.30	725.00	06/1999 -	07/2012	9.35
163	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	550.00 -	1,566.00	- -	-	184.73

(July 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
164	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	494.92	- -	-	67.77
165	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH- KODINAR (GC) - [N22000143]	04/1994	320.66 -	913.48	- -	-	184.87
166	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	685.17	- -	-	53.63
167	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	3,500.00	- -	-	68.05
168	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	02/2020	226.98
169	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	262.00	- -	-	10.58
170	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]	04/2013	456.00 -	855.16	- -	-	87.54
171	RATANGARH-SARDARSAHAR (MM OF SADULPUR- BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	-	17.92
172	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	218.39	- -	-	2.34
173	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR- BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	02/2019	226.23
174	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00	- -	-	62.32
175	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00	- -	12/2019	82.25
176	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
177	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44
178	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	03/2016	88.40
179	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	12/2017	41.36
180	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
181	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
182	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	- -	-	338.91
183	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
184	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00 -	1,887.90	- -	03/2019	5.00
185	ATTIPPATTU-PUTTUR - [N22000184]	04/2008	446.87 -	528.00	- -	-	18.16

(July 2015)

(July 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
186	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52	1,200.00	-	-	129.22
187	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00	1,500.00	-	-	78.78
188	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68	556.64	-	-	180.17
189	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]	04/1998	271.24	520.00	-	-	91.71
190	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39	1,280.83	-	-	55.74
191	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14	346.15	-	-	28.14
192	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42	563.13	-	03/2019	154.33
193	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00	1,242.25	03/2007	03/2016	38.80
194	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00	886.65	-	03/2018	251.85
195	DIMAPUR-TIZIT NL - [N22000196]	04/2013	4,274.00	4,487.70	-	03/2020	5.00
196	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77	441.45	-	03/2018	110.44
197	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55	288.81	-	03/2018	1.86
198	ERODE-PALANI - [N22000199]	04/2008	288.57	603.22	-	-	109.04
199	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41	450.00	-	-	173.71
200	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	247.00	951.24	-	03/2015	285.12
201	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72	222.95	-	-	16.29
202	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02	5,307.90	-	03/2020	30.00
203	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22	679.57	-	03/2018	180.56
204	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52	394.28	-	03/2017	63.25
205	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82	435.58	-	03/2018	162.68
206	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]	04/1999	523.17	1,653.55	-	03/2018	216.06
207	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12	453.10	-	03/2018	45.17

(July 2015)

(July 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
208	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211	04/2012	246.07 -	364.06	- -	03/2019	47.95
209	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213	04/2012	632.68 -	816.55	03/2016 -	03/2016	29.06
210	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215	04/2011	601.43 -	800.00	- -	-	33.02
	Total		81,685.74 -	208,168.14			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
211	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 -	361.00	02/2009 -	-	28.93
212	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	04/2009 -	-	92.75
213	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	11/2008 -	12/2015	80.68
214	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	331.23	07/2009 -	-	68.99
215	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	-	106.50
216	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063	12/2003	217.61 -	309.56	04/2010 -	01/2016	42.25
217	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221	12/2003	155.00 -	201.66	09/2008 -	09/2015	30.10
218	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	02/2010 -	-	2.29
	Total		2,586.46 -	4,438.02			
	<u>SHIPPING AND PORTS</u>						
219	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016	11/2007	1,228.00 -	1,460.00	12/2010 -	-	18.89
220	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059	03/2007	245.67 -	373.22	04/2009 -	-	51.92
221	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	01/2007	366.39 -	669.46	12/2010 -	01/2016	82.72
	Total		1,840.06 -	2,502.68			
	<u>STEEL</u>						
222	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	10/2016	42.39
223	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067	10/2005	8,692.00 -	12,291.00	10/2009 -	04/2015	41.41

(July 2015)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	Total		9,035.00 -	12,779.40			
	URBAN DEVELOPMENT						
224	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00 -	11,609.00	06/2011 -	-	81.53
	Total		6,395.00 -	11,609.00			
	Grand Total		252,530.77	463,195.47			

Details of Delayed Projects w.r.t. Original and Revised Schedule

(July 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL, TAMIL NADU	12/2001	13,171.00 17,270.00	17,270.00	20,713.00	12/2008 -	10/2015	82	31.12	Slippage of commitments by M/s Atomstroy export, Russian Federation.
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVINI, TAMIL NADU	09/2003	3,492.00 5,677.00	5,677.00	5,031.21	09/2010 09/2016	09/2016	72	62.57	
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 -	11,459.00	6,853.00	12/2015 -	10/2017	22	0	Late receipt of financial sanction.
4	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 -	12,320.00	4,669.00	12/2016 -	05/2018	17	0	Delay in supply of equipments from various vendors.
	Total		40,442.00 -	46,726.00	37,266.21					
	<u>CIVIL AVIATION</u>									
5	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT (MOHALI) PH - II - [N04000070]JAAI, CHANDIGARH	02/2011	452.00 489.00	489.00	468.24	03/2015 -	07/2015	4	8.19	
6	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]JAAI, MULTI STATE	10/2012	217.60 -	244.10	0.04	03/2015 -	09/2015	6	12.18	
7	CONSTRUCTION OF NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT - [N04000050]JAAI, SIKKIM	01/2009	309.46 -	309.46	357.35	01/2011 06/2016	09/2017	80	0	Terminal Building work stopped by local residents demanding compensation citing damages to their properties.
	Total		979.06 -	1,042.56	825.63					
	<u>COAL</u>									
8	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC, TAMIL NADU	10/2004	2,030.78 3,583.77	3,583.77	3,213.77	06/2009 03/2013	07/2015	73	76.47	The project is delayed right from the beginning, due to the fact that 250 MW CFBC Boilers are first of its kind in India. The project also got delayed due to the slow execution of work by M/s BHEL, the Main plant package contractor.

(July 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
9	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]JNLC,TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	6,355.68	03/2012 05/2014	08/2015	41	34.63	Delay in finalization of sub-contractors and mobilization of resources. Delay in release of work front by M/s BHEL to other contractors like ABB and L&T has delayed the start-up power supply. Inadequate manpower deployment by BHEL. Delay in initial commencement of civil works for boiler. Delay in Engineering.
10	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]JNLC,TAMIL NADU	04/2012	364.75 -	364.75	159.12	10/2014 -	08/2015	10	0	The firm should have commissioned all the 34 WTGs as per the Fourth EOT given upto 30.06.2015. There is delay in manufacturing and supply of WTG equipments and completion of foundations.
11	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]JCL,ODISHA	01/2005	302.96 -	302.96	146.90	03/2010 -	03/2016	72	0	
12	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,863.12	03/2014 -	03/2016	24	0	
13	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,664.33	03/2014 -	03/2016	24	0	
14	KRISHNASHILA (NCL) (4MTY) - [N06000007]JNCL,UTTAR PRADESH	06/2011	789.88 741.62	741.62	480.93	03/2013 -	03/2016	36	-6.11	
15	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]JNCL,MADHYA PRADESH	06/2011	746.04 535.10	535.10	382.96	03/2015 -	03/2016	12	-28.27	
16	MAGADH OC 20 MTY (CCL) - [N06000015]JCL,JHARKHAND	08/2008	706.40 -	706.40	77.19	07/2012 -	03/2016	44	0	test
17	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,TELANGANA	12/2009	212.34 1,228.39	1,228.39	859.79	03/2013 09/2012	03/2016	36	478.5	
18	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35 -	462.35	298.70	03/2014 -	03/2016	24	0	

(July 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
19	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82	153.82	59.12	03/2014	03/2016	24	0	(1) Delay in finalization of Global tender. (2) Delay in rehabilitation and Resettlement activity due to resistance by villagers.
20	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97	418.97	365.16	03/2012	03/2016	48	0	
21	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78	209.78	74.10	03/2015	03/2016	12	0	
22	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19	181.19	36.60	03/2012	03/2016	48	0	
23	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50	321.50	207.27	03/2014	03/2016	24	0	
24	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51	163.51	35.92	03/2011	03/2016	60	0	
25	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98	210.98	147.70	03/2013	03/2016	36	0	
26	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68	264.68	144.13	03/2012	03/2016	48	0	
27	MURADIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88	339.88	10.98	04/2014	03/2016	23	0	
28	RG OC -III EXTENSION (PHASE - II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01	365.01	6.56	06/2015	03/2016	9	0	
29	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45	289.45	97.48	05/2014	10/2016	29	0	
30	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82	269.82	40.12	04/2014	11/2016	31	0	
31	ASHOK EXPN OCP CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	341.63 341.63	341.63	124.95	03/2011	03/2017	72	0	i) Law & Order ii) Coal evacuation problems

(July 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
32	JHANJRA R-VI SEAM PSLW - [N06000020]ECL, WEST BENGAL	11/2006	287.18 -	287.18	225.39	03/2011 -	03/2017	72	0	Lol for procurement of transporting equipment was issued on 14-01-2015 subject to the pending approval of CIL Board. It was placed before CIL Board on 22-02-2015. CIL Board advised to prepare a comprehensive report of Jhanjra. Further ECL has appealed to CIL for approval of advance actions for procurement of transporting equipment on 09-05-2015 citing the comprehensive report is under process of approval by ECL Board. Finally CIL Board approved the advance action proposal on 12-05-2015.
33	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]JNCL, MADHYA PRADESH	10/2007	259.40 -	259.40	25.10	03/2012 -	03/2017	60	0	
34	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL, ODISHA	12/2007	457.77 -	457.77	181.15	03/2013 -	03/2017	48	0	
35	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]MCL, ODISHA	12/2007	172.08 -	172.08	148.48	03/2010 -	03/2017	84	0	
36	KAKATIYA LONGWALL - [N06000048]SCCL, TELANGANA	12/2008	453.63 -	453.63	99.71	12/2012 -	03/2017	51	0	
37	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL, ODISHA	08/2008	207.28 -	207.28	191.76	03/2012 -	03/2017	60	0	
38	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.53 -	479.63	173.59	03/2013 -	03/2017	48	.02	
39	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCCL, JHARKHAND	12/2007	179.87 -	179.87	-	03/2012 -	03/2017	60	0	
40	KARMA OCP (1.0 MTY) - [N06000088]CCCL, JHARKHAND	06/2009	162.46 -	162.46	-	03/2014 -	03/2017	36	0	
41	KALYANIKHANI OPENCASE PROJECT - [N06000101]SCCL, TELANGANA	07/2012	417.33 -	417.33	13.78	07/2016 -	03/2017	8	0	
42	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL, TELANGANA	10/2006	249.03 -	249.03	73.99	03/2012 -	03/2018	72	0	
43	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29 -	242.29	0.03	03/2015 -	03/2018	36	0	

(July 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
44	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL, TELANGANA	07/2011	447.06 -	447.06	29.03	03/2015 -	03/2018	36	0	
45	NEYVELI NEW THERMAL POWER PROJECT (2X500 MW) - [N06000095]NLC, TAMIL NADU	06/2011	5,907.11 -	5,907.11	1,008.61	12/2015 04/2018	04/2018	28	0	Project was delayed due to re-tendering of SG & Aux. package.
46	RCE OF INDARAM OCP (1.20 MTPA) - [N06000093]SCCL, TELANGANA	07/2011	162.76 -	162.76	1.31	03/2015 -	03/2019	48	0	
47	MOONIDIH XV SEAM UG - [N06000098]JBCCL, JHARKHAND	08/2011	1,230.27 -	1,230.27	42.39	04/2015 04/2019	04/2019	48	0	
48	TALABIRA OCP - [N06000043]JMCL, ODISHA	03/2008	447.72 -	447.72	52.36	03/2016 -	03/2020	48	0	
49	JAGANNATHPOR OCP (3.00 MTY) - [N06000075]SECL, CHHATISGARH	09/2008	152.43 -	152.43	24.72	03/2015 -	03/2020	60	0	
50	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH	07/2008	178.44 -	178.44	0.30	03/2014 -	03/2020	72	0	
51	GOPAL PRASAD OCP (15MTY) - [N06000042]JMCL, ODISHA	02/2008	395.87 -	395.87	76.74	03/2015 -	03/2021	72	0	
	Total		31,159.10 -	35,167.24	19,221.02					
	STEEL									
52	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL, ODISHA	10/2012	160.48 -	160.48	132.35	09/2014 -	07/2015	10	0	
53	CAPTIVE POWER PLANT - 2 - [N12000087]JINL, ANDHRA PRADESH	02/2011	677.00 -	677.00	523.82	09/2013 -	07/2015	22	0	
54	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL, JHARKHAND	05/2010	6,325.00 -	6,325.00	5,164.71	12/2011 -	08/2015	44	0	
55	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC, KARNATAKA	02/2011	898.55 -	898.55	390.19	05/2013 01/2015	08/2015	27	0	
56	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODISHA - [N12000079]SAIL, ODISHA	06/2012	237.09 -	237.09	192.84	12/2014 -	09/2015	9	0	
57	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHHATISGARH - [N12000078]SAIL, CHHATISGARH	07/2012	332.65 -	332.65	205.40	08/2014 -	11/2015	15	0	
58	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL, MAHARASHTRA	12/2011	187.33 -	187.33	163.67	10/2013 -	12/2015	26	0	

(July 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
59	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]SAIL, WEST BENGAL	11/2012	313.05 -	313.05	267.06	06/2015 -	12/2015	6	0	
60	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, CHHATISGARH	08/2010	17,265.00 -	17,265.00	14,537.66	03/2013 -	03/2016	36	0	
61	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]JINL, ANDHRA PRADESH	07/2011	877.73 -	877.73	263.16	07/2015 -	03/2016	8	0	
62	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC, CHHATISGARH	01/2010	15,525.00 -	15,525.00	7,580.18	05/2015 12/2016	12/2016	19	0	
63	SMS-1 CONVERTERS REVAMPING - [N12000090]JINL, ANDHRA PRADESH	05/2012	404.16 -	404.16	159.15	07/2015 -	03/2017	20	0	
	Total		43,203.04 -	43,203.04	29,580.19					
	<u>PETROCHEMICALS</u>									
64	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, ASSAM	04/2006	5,460.61 8,920.00	9,833.52	8,784.45	04/2012 12/2013	09/2015	41	80.08	• Lack of adequate and effective supervision by the EPMC, M/s EIL. • Misplacement / mismanagement of free issue materials.
	Total		5,460.61 -	9,833.52	8,784.45					
	<u>PETROLEUM</u>									
65	LPG TERMINAL AT KOCHI - [N16000171]IOCL, KERALA	12/2012	607.06 -	607.06	57.94	01/2016 -	04/2017	15	0	
66	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]ONGC, MAHARASHTRA	03/2012	5,608.40 -	5,608.40	4,456.55	05/2015 05/2015	08/2015	3	0	
67	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL, MAHARASHTRA	03/2012	1,419.00 -	1,419.00	1,205.72	12/2014 -	08/2015	8	0	

(July 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
68	102 MW WIND POWER PROJECT - [N16000119]ONGC, RAJASTHAN	07/2010	1,106.00 678.02	678.02	405.00	06/2012 03/2015	09/2015	39	-38.7	-Commissioning is pending as NOC is awaited from the MOD (air force) -ROW problem at site due to intervention of local villagers. Work commenced under police protection. -Scope revision and delay in award of work.
69	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL, TAMIL NADU	12/2012	279.00 -	279.00	160.87	12/2014 -	09/2015	9	0	Pre-commissioning activities are in progress. Hook up shutdown for Mounded bullet pipelines are to be done during existing refinery-III S/d which is planned in July 2015
70	PARADIP REFINERY PROJECT - [N16000058]IOCL, ODISHA	02/2009	29,777.00 34,555.00	34,555.00	29,606.96	11/2012 11/2013	10/2015	35	16.05	
71	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL, ODISHA	07/2009	199.75 -	239.73	192.28	07/2013 -	10/2015	27	20.02	
72	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]ONGC, MULTI STATE	10/2013	429.06 429.00	429.06	357.59	10/2014 10/2015	10/2015	12	0	nil
73	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL, MULTI STATE	04/2010	270.00 -	215.66	-	06/2012 11/2015	11/2015	41	-20.13	Delay in placement of order for 2 nos drilling rigs. One of the bidder went to court in anticipation of disqualification of their bid
74	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC, MULTI STATE	06/2007	736.65 -	736.65	481.63	09/2011 12/2015	12/2015	51	0	-Delay in preparation of drawing and additional model testing of Hull form in Austria . - Shortage of skilled manpower at contractor's end. - Inadequate ancillary/sub-contractors at the location -Lack of planning to match resources to work targets. - Change in delivery location. -Delay in procurement of steel by PSL.

(July 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
75	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA	12/2009	1,584.00 -	1,584.00	1,262.55	08/2015 -	12/2015	4	0	
76	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE	06/2010	2,523.00 2,523.00	2,523.00	1,528.40	01/2014 12/2015	12/2015	23	0	-Slow progress by contractor. - Slow progress by the contractor in laying of pipelines. - Delay in drilling of some wells due to non-availability of light rig.
77	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	317.64 -	240.95	117.49	09/2012 12/2015	12/2015	39	-24.14	-Slow progress in civil work and fabrication work due to less resource mobilization. -Unresolved commercial issues between M/s UEM and NSF Vendor. -Delay in finalization of Process package leading to delay in engg and procurement services. -Delay in delivery of Nut Shell filters and internal of IGF units.
78	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 1,256.72	1,256.72	896.92	05/2013 06/2014	12/2015	31	45.83	-Increase in scope of work -Delay in procurement of steel and fabrication of legs by the contractor.
79	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,MULTI STATE	08/2011	586.00 -	586.00	342.83	08/2015 -	12/2015	4	0	
80	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 686.58	686.58	478.03	04/2015 04/2015	12/2015	8	-39.69	
81	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96 -	191.96	92.09	05/2015 -	12/2015	7	0	
82	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]JSPRL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	979.86	10/2011 -	01/2016	51	67.62	Some difficulties being faced during Cavern Acceptance Test, which is in progress.
83	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]JSPRL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,427.40	01/2012 -	01/2016	48	70.49	Progress is slow due to heavy rains during the period.
84	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	1,173.22	09/2012 -	03/2016	42	0	

(July 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
85	VKPL UPGRADE AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32	463.32	283.90	06/2011 03/2012	03/2016	57	0	
86	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	1,217.33	03/2015 05/2016	05/2016	14	29.42	Pipeline package: Non-performance by the contractor: The contractor of pipeline package was served notice of termination of the contract on 11.01.2014 and again on 07.03.2014 in view of contractor's inability to execute the work on time. The contractor served notice of arbitration on 01.10.2014 to settle disputes. ONGC proposed resolution of disputes through Outside Expert Committee (OEC) on 03.11.2014, which the contractor agreed on 07.11.2014. The contractor, thereafter, proposed certain pre-conditions to start the work and since then holding up the work. Delay in conversion of Rig Sagar Laxmi to MOPU due to financial issues and non-performance of the contractor.
87	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 2,592.17	2,592.17	541.46	05/2014 05/2016	05/2016	24	0	

(July 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
88	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17 600.17	600.17	375.14	12/2014 05/2015	05/2016	17	0	Pipeline package: Non-performance by the contractor: The contractor of pipeline package was served notice of termination of the contract on 11.01.2014 and again on 07.03.2014 in view of contractor's inability to execute the work on time. The contractor served notice of arbitration on 01.10.2014 to settle disputes. ONGC proposed resolution of disputes through Outside Expert Committee (OEC) on 03.11.2014, which the contractor agreed on 07.11.2014. The contractor, thereafter, proposed certain pre-conditions to start the work and since then holding up the work.
89	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE	01/2012	352.49 -	352.49	128.12	03/2014 05/2016	05/2016	26	0	-Design platform integrity issue was raised by the contractor which required review of integrity analysis and this took time in resolution. - Clubbing of project facilities alongwith C-26 Cluster development project. - slow progress by the contractor.
90	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	723.64	-	03/2013 06/2016	06/2016	39	0	
91	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	913.00	424.47	08/2015 -	06/2016	10	0	
92	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	1,200.00	281.58	03/2015 11/2015	06/2016	15	37.72	Heavy rain in Assam.Refloating of tender will have impact on timeline
93	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]IOCL,BIHAR	04/2013	480.00 -	480.00	44.48	02/2016 -	07/2016	5	0	

(July 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
94	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU	02/2011	3,110.36	3,110.36	799.71	11/2015 07/2016	07/2016	8	0	Restricted working environment due to nearby operating plants, availability of limited space for storage & fabrication, Restricted timings for radiography activities etc.. were affecting the progress of the work.
95	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 462.79	462.79	237.49	10/2014 10/2016	10/2016	24	49.38	
96	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,KARNATAKA	02/2012	666.00 838.08	838.08	481.49	11/2015 11/2016	11/2016	12	25.84	
97	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 2,378.89	2,378.89	1,781.40	03/2013 03/2016	03/2017	48	-3.5	-Substantial time taken for mobilization by survey and other agency. -ROU acquisition and issue related to payment -Delay in forest clearance. -Inadequate manpower at working sites affected the construction progress. -Local problem and court cases by tea gardener. -Slow progress in engineering and procurement.
98	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC,MULTI STATE	04/2013	284.82	284.82	-	04/2015 05/2017	05/2017	25	0	DELAY IN TENDERING PROCESS. ISSUES RAISED BY BIDDERS.
99	AHMEDABAD REDEVELOPMENT PROJECT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10	1,916.10	1,161.74	12/2014	12/2017	36	0	
100	MEHESANA REDEVELOPMENT PROJECT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00	3,823.00	1,076.57	04/2015 12/2017	12/2017	32	0	
101	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]ONGC,MAHARASHTRA	12/2012	3,513.07 4,619.94	4,619.94	336.33	02/2016 12/2017	12/2017	22	31.51	nil
102	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE	05/2013	4,124.35	4,124.35	75.24	04/2016 04/2016	12/2017	20	0	retendering of various packages.

(July 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
103	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]OCL, WEST BENGAL	03/2014	3,076.00 -	3,076.00	98.00	09/2017 -	12/2017	3	0	
104	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL, MULTI STATE	07/2009	3,957.00 3,561.00	3,561.00	5.92	01/2013 -	12/2018	71	-10.01	
105	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC, GUJARAT	11/2010	2,189.63 -	2,189.63	1,035.48	12/2014 -	12/2018	48	0	
106	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC, D & N HAVELI	08/2014	6,086.08 -	6,086.08	84.54	05/2019 03/2020	03/2020	10	0	nil
	Total		95,729.95 -	103,011.27	55,693.72					
	<u>POWER</u>									
107	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO, TRIPURA	07/2009	421.01 1,007.68	1,007.68	902.86	07/2013 -	08/2015	25	139.35	1) Although Trial operation for the gas turbine was started on 28th July 2015, the same could not be continued due to inability on part of ONGC to sustain the required inlet pressure of Gas from 29th July 15 onward. 2) As such Trial operation of the Gas Turbine remain suspended till resumption of Gas supply by ONGC at required pressure. 3) Commercial operation of the Gas Turbine that was scheduled for mid August 2015 is now uncertain.
108	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND - III GEN. PROJ. - [N18000076]PGCIL, MULTI STATE	03/2010	4,672.99 -	4,672.99	3,756.67	11/2012 -	08/2015	33	0	Delayed due to forest clearance, wild life sanctuary clearance & ROW problems.
109	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ. IN ORISSA PART-C - [N18000096]PGCIL, MULTI STATE	03/2011	2,569.25 3,105.51	3,105.51	2,854.67	03/2014 06/2015	08/2015	17	20.87	Involvement of forest, Wildlife clearance & severe ROW problem.
110	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL, MADHYA PRADESH	03/2012	213.78 -	213.78	201.04	03/2014 -	08/2015	17	0	

(July 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
111	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,MULTI STATE	09/2012	1,508.74 -	1,508.74	950.08	03/2015 -	09/2015	6	0	Delay in land acquisition of New Kudgi Sub station.
112	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19 -	2,743.19	2,783.30	12/2013 -	09/2015	21	0	Delayed due to forest clearance.
113	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	142.10	01/2013 -	09/2015	32	0	Delay in land acquisition of Kishanganj Sub station.
114	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	2,085.56	08/2014 -	09/2015	13	0	Delayed due to delay in land acquisition of Varansai S/stn. & forest clearance.
115	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	529.30	02/2014 -	09/2015	19	0	Severe ROW problem faced.
116	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL,MULTI STATE	02/2012	1,927.16 -	1,927.16	1,533.67	10/2014 -	09/2015	11	0	Severe ROW problem faced.
117	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	194.52	04/2015 -	09/2015	5	0	Delay in land acquisition of Varansai S/stn.
118	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 2,348.37	2,348.37	1,878.34	03/2013 06/2015	10/2015	31	13.18	Delayed due to forest involvement & severe ROW problem.
119	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 689.03	689.03	490.72	07/2013 05/2015	11/2015	28	-8.45	Delayed due to forest clearance which is still awaited.
120	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	487.49	379.02	06/2014 -	11/2015	17	0	Severe ROW problem in Karnataka & down stream system being executed by State not available.
121	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,KARNATAKA	03/2005	1,007.16 -	1,007.16	1,002.91	12/2007 12/2009	12/2015	96	0	Delayed due to severe ROW problem in Karnataka.
122	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,492.46	11/2013 -	12/2015	25	0	Delay in land acquisition of Kishanganj S/stn. and ROW problem

(July 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
123	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	464.61	11/2013 -	12/2015	25	0	Delay in forest clearance & delay in land acquisition of Chandwa Sub station.
124	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 346.79	346.79	285.47	08/2014 06/2015	12/2015	16	16.63	Severe ROW problem in Bengaluru.
125	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	526.22	11/2014 -	12/2015	13	0	Delayed due to forest clearance & severe ROW problem.
126	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	2,159.07	1,894.05	09/2008 03/2012	03/2016	90	21.34	Delayed due to severe ROW problem in Kerala due to compensation issues.
127	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 721.81	721.81	521.59	09/2010 06/2013	03/2016	66	51.1	
128	PARE HYDRO ELECTRIC PROJECT - [N18000045]NPEPCO,ARUNACHAL PRADESH	12/2008	573.99 1,487.49	1,487.49	1,016.43	08/2013 -	03/2016	31	159.15	Law & order problem from time to time and change in geotechnical parameters necessitating revision of side slopes.
129	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	468.66	11/2011 -	03/2016	52	0	Severe ROW problem in western UP due to high compensation demand.
130	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	331.57	02/2012 -	03/2016	49	0	Severe ROW problem in western UP due to high compensation demand.
131	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	4,133.98	10/2012 -	03/2016	41	0	Delay in forest clearance and contractual issue.
132	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 -	4,404.57	1,959.15	01/2015 -	03/2016	14	0	Wildlife sanctuary clearance awaited & delay in land acquisition of Alipurduar Station.
133	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	2,176.10	12/2012 -	03/2016	39	0	Delayed due to forest clearance, stiff resistance/local disturbance and contractual issues.
134	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,056.29	08/2012 -	03/2016	43	0	Delayed due to poor performance by contractor.

(July 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
135	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	739.34	11/2012 -	03/2016	40	0	Delayed due to severe ROW problem in western UP demanding high compensation.
136	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,318.22	04/2013 -	03/2016	35	0	Delayed due to severe ROW problem in western UP demanding high compensation.
137	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHHATTISGARH - [N18000112]PGCIL,CHHATTISGARH	11/2011	2,127.51 -	2,127.51	2,211.93	07/2014 -	03/2016	20	0	Delay in forest clearance (Stage - I awaited) & severe ROW problem.
138	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHHATTISGARH - [N18000116]PGCIL,CHHATTISGARH	12/2011	1,746.65 2,228.71	2,228.71	1,265.43	08/2014 12/2015	03/2016	19	27.6	Delay in forest clearance and NOC for wildlife awaited for Aurangabad - Padghe and anticipated delay in completion of Kudus S/stn. executed by MSETCL.
139	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATTISGARH	01/2012	1,422.85 -	1,422.85	1,181.42	01/2015 -	03/2016	14	0	Delay in forest clearance.
140	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	2,456.41	10/2014 -	03/2016	17	0	Delay in land acquisition of Kanpur sub station.
141	KBUNL-MUZAFFARPUR TPP STAGE-II- SUBSIDIARY (2X195 MW) - [N18000191]NTPC,BIHAR	03/2010	3,984.03 -	3,984.03	2,916.06	01/2013 -	03/2016	38	0	Non performance of Civil, Swyd, CHP, AHP agencies
142	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]NHPC,WEST BENGAL	09/2005	1,061.38 -	1,929.15	1,813.21	09/2009 -	06/2016	81	81.76	1. Initial delay in handing over of forest land & start of work 2. Bandh/ closure by locals , political outfits like GJMM and its effect 3. Due to inordinate delay and extended stay, BOQ rates became unworkable and resulted in cash deficit of Civil Contractor. 4. Delay in award of E&M contract due to clarification regarding participation of Chinese firm

(July 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
143	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATISGARH	05/2011	1,961.87 -	1,961.87	1,724.75	05/2014 -	06/2016	25	0	Delay in land acquisition of Champa Sub station.
144	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,826.86	09/2014 -	06/2016	21	0	Severe ROW problem in Karnataka & contractual issues.
145	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	77.53	09/2014 -	06/2016	21	0	Severe ROW problem.
146	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATISGARH	03/2012	9,569.76 -	9,569.76	4,720.39	06/2015 -	06/2016	12	0	Delay in land acquisition of Champa Sub station.
147	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	844.85	12/2015 -	06/2016	6	0	Severe ROW problem & huge forest involvement.
148	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	240.70	06/2015 -	08/2016	14	0	Commissioning linked to Angul – Srikakulam line & readiness of Srikakulam – Vemagiri line being executed under TBCB rout (sch Aug 16) being expedited.
149	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	791.33	06/2015 -	08/2016	14	0	Forest clearance awaited and 01 pkg. re-tendered & award in Jun 15.
150	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM	07/1998	368.72 1,381.71	1,381.71	857.94	07/2006 12/2015	10/2016	123	274.73	Progress of work is affected due to rain and slippery road condition.

(July 2015)

(July 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
151	KISHANGANGA HEP (3X110 MW) - [N18000031]JNHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,497.72	4,056.08	01/2016 -	11/2016	10	50.95	1. Law & order problem in the project area and Kashmir Valley. 2. Delay in settlement of R&R plan of the project which is pending with J&K State Govt. for approval and strike by PFA's 3. Due to delay decision of International Court of Arbitration
152	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	-	04/2016 -	11/2016	7	0	Delay in supply.
153	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	11,005.30	08/2013 -	12/2016	40	0	Delayed due to severe ROW problem, forest clearance & disturbance in NER.
154	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	1,127.43	11/2012 -	12/2016	49	0	Delay in land acquisition of Sub stations.
155	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 6,476.34	6,476.34	3,964.79	12/2009 03/2017	03/2017	87	159.38	REASONS OF DELAY: 1) Redesign of Dam parameters: 2) Geological surprises: 3) Realignment of HPT 4) Slope Stabilization of Power House area 5) Flash floods / rains 6) Deviation in works 7) Contractual Issues 8) Major deviation in encountered geology than that envisaged 9) Permission for Quarry operation yet to be received from Govt. of Arunachal Pradesh 10) Restriction on release of equity

(July 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
156	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC, ASSAM	01/2008	4,375.35 6,749.18	6,749.18	5,365.00	09/2011 -	03/2017	66	54.25	-Frequent Bandh calls by local outfits (Total Bandh-262 days) leading to stoppage of work at site for more than 500 days. -Eruption of ethnic violence in Jul-12, May-14 & Dec-14 (41 days) leading to stoppage of work for 171 days. -Poor performance of BOP/Civil contractors due to geo-political situation in the region.
157	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC, BIHAR	01/2007	5,353.00 -	5,353.00	4,753.79	05/2014 -	06/2017	37	0	- Delay in balance land acquisition. - Law & order problem.
158	SOLAPUR STPP - [N18000133]NTPC, MAHARASHTRA	03/2012	9,395.18 -	9,395.18	5,138.00	11/2016 -	08/2017	9	0	Delay of 12 months in Engg. & supplies by BGR which has led to a consequent delay of 12 months in erection.
159	DHUKWAN SMALL HYDRO PROJECT - [N18000189]JTHCIL, UTTAR PRADESH	05/2011	195.42 -	195.42	29.03	02/2014 -	09/2017	43	0	Law and order: Resistance by locals and pressure groups demanding works at rates of their choice.
160	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC, UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	3,530.14	12/2016 -	09/2017	9	0	Delay of 12 months in Engg. & supplies by BGR which has led to a consequent delay of 12 months in erection.
161	BARH STPP(3X660MW) NTPC - [180100242]NTPC, BIHAR	02/2005	8,692.97 15,095.67	15,095.67	10,764.00	01/2011 10/2014	03/2018	86	73.65	Non performance of Russian agency M/s TPE & M/s PM. TPE stopped work from Oct-2013 and the contract of Ms TPE was terminated on 14.01.15.
162	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]JTHCIL, UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	1,335.62	07/2010 02/2016	05/2018	94	79.77	1. Non availability of Asena Quarry 2. 4.668 Ha. Land diversion case for dumping area at Village Chopra.

(July 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
163	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC, HIMACHAL PRADESH	09/2002	3,919.59 -	7,818.68	5,142.86	09/2009 -	12/2018	111	99.48	1. Initial delay in start of Dam works due to delay in Revised Forest clearance 2. Burial of TBM during Nov, 06. Heavy ingress of water with silt from TBM face. Treatment of shear zone, 3. Back hill slope failure of Power House three times, 4. Ban on use of aggregates by Hon'ble High Court, Shimla
164	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC, UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	2,512.00	03/2013 -	12/2018	69	29.14	-Flash Flood in Jun-13 in Uttarakhand leading to damage of coffer dam & approach road. - Tunnel Boring Machine stuck up thrice & L&T Alpine JV did not perform leading to termination of contract. - Head Race Tunnel (HRT) Package is under retender.
165	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL, UTTARAKHAND	08/2008	2,491.58 -	3,745.08	701.40	06/2013 -	12/2019	78	50.31	Court case.
	Total		144,523.04 -	171,759.47	120,423.15					
	<u>HEAVY INDUSTRY</u>									
166	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]HIPE, MULTI STATE	04/2011	1,718.00 -	3,827.30	-	09/2011 -	12/2017	75	122.78	
	Total		1,718.00 -	3,827.30	.00					
	<u>RAILWAYS</u>									
167	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII-MUSORE (SWR) - [N22000107]SWR, KARNATAKA	04/2007	482.00 -	874.57	730.11	03/2013 -	09/2015	30	81.45	Commissioning target is subject to handing over of land by GoK.
168	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]JER, WEST BENGAL	04/1999	207.52 -	207.52	223.44	12/2012 -	09/2015	33	0	

(July 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
169	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]JECR,BIHAR	04/2002	921.00 -	2,363.00	1,691.12	03/2009 12/2012	10/2015	79	156.57	Railway bridge targeted for commissioning in October, 2015 (resettlement of 3 families is involved.) Road bridge would take time as there are issues in land acquisition.
170	ETAWAH-MAINPURI (NL),NCR - [220100318]JNCR,UTTAR PRADESH	04/1997	120.00 245.39	245.39	249.33	12/2008 -	10/2015	82	104.49	
171	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	335.00	230.67	06/2004 -	12/2015	138	72.62	Law & Order issue affected the work progress. Material Modification for Electrification estimate are awaited from Jharkhand Govt.
172	PATNA GANGA BRIDGE (NL), ECR - [220100308]JECR,BIHAR	04/2001	624.47 -	2,921.00	2,521.72	10/2007 12/2012	12/2015	98	367.76	Railway bridge targeted for commissioning in October, 2015. However Road bridge would take time as there are issues in land acquisition.
173	BHOPAL BINA 3D LINE DOUBLING - [N22000077]JRVNL,MADHYA PRADESH	09/2007	687.20 -	800.00	793.71	03/2010 -	12/2015	69	16.41	
174	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 495.44	1,781.98	440.08	03/2004 12/2010	03/2016	144	259.68	Total length of railway line is 27 km. Land hasnot been acquired in 2.7 km length between Kharkopar and Ranjanpada (25 hectare private land and also forest land). Construction is in progress in part of the line and only part commissiong can be done.

(July 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
175	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	275.08	141.55	03/2012 12/2013	03/2016	48	60.77	Initially the electrification of Khurja-Meerut-Saharanpur section was sanctioned in 1996-97 and subsequently the work was frozen. In 2007-08 electrification work of Khurja-Meerut-Saharanpur was defroze and Ghaziabad-Meerut section also included as a material modification. Authorisation has been received on 13-08-2014 to run electric trains on Khurja-Meerut city. The electrification work on the balance portion is in progress and planned for completion by Nov 2015 (Meerut -Saharanpur).
176	KATAKHAL TO BHAIIRABI - [N22000126]JNFR,ASSAM	04/1998	227.90 200.00	331.40	182.22	12/2012 -	03/2016	39	45.41	
177	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]JNFR,ASSAM	04/1996	1,676.31 -	5,500.00	4,734.45	03/2009 -	03/2016	84	228.1	Line commissioned and freight train operations commenced. Passenger operations to commence in August 2015.
178	DANGOAPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	583.00	144.66	12/2015 -	03/2016	3	88.4	Work delayed due to foundation problem.
179	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]JNFR,TRIPURA	04/1999	895.00 575.00	1,242.25	1,005.81	03/2007 -	03/2016	108	38.8	Section will be completed after Lumding-Silchar, Badarpur- Kumarghat GC Project.
180	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	204.56	03/2016 -	06/2016	3	0	Work hampered due to encroachment on Railway land along the proposed metro alignment.
181	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	230.00	68.67	03/2015 -	12/2016	21	53.44	
182	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]JNR,UTTAR PRADESH	04/2006	325.00 -	1,564.54	420.71	03/2010 03/2017	03/2017	84	381.4	
183	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]JMRT,MAHARASHTRA	04/2012	714.10 -	714.10	65.93	04/2016 -	03/2017	11	0	

(July 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
184	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR, ASSAM	09/1997	1,500.00 1,000.00	4,996.19	3,410.06	04/2008 03/2014	06/2017	110	233.08	
185	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR, BIHAR	09/2001	492.98 -	1,727.27	743.74	12/2010 -	03/2018	87	250.37	Work affected due to fund constraint.
186	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	733.00 733.00	2,531.34	1,732.43	12/2008 -	03/2018	111	245.34	Work is affected due to land problems. State Govt. has been requested to expedite handing over of land to Railways for early commissioning of the line.
187	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA	04/2008	813.34 813.34	2,876.00	823.83	03/2014 -	03/2018	48	253.6	Supreme court approval is required for NBWL clearance of 9.94 Hect Trishna Wild life Sanctuary.
188	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	619.34 619.34	2,820.25	199.31	04/2014 03/2015	03/2018	47	355.36	
189	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	4,874.58	1,911.65	03/2016 -	06/2018	27	0	Phase- I of the project is to be completed by June, 2018 subject to availability of land and funds. Target for phase-II cannot be fixed since the works are held up due to State Govt's proposal for change of alignment of the underground portion.
190	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	19,565.00	10,658.34	11/2002 -	12/2018	193	682.6	
191	JIRIBAM TO IMPHAL (TUPIJ)(NL)(NEFR) - [220100288]NFR, MANIPUR	04/2003	727.56 727.56	6,570.75	2,787.99	03/2011 03/2014	03/2019	96	803.12	
192	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 6,821.29	7,986.04	2,443.62	03/2014 03/2019	03/2019	60	50.68	Fund constraint affecting the progress of projects.
193	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, MULTI STATE	02/1997	386.30 1,157.54	1,544.40	590.26	03/1998 -	12/2019	261	299.79	Progress is going as per the allotment of budget grant.
194	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	2,371.85	486.25	03/2005 12/2008	12/2019	177	2019.62	Local disturbance and fund constraint affected the work progress.
195	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97 1,013.74	1,428.00	466.36	06/2005 07/2011	12/2019	174	385.76	In Kanthi-Egra section land acquisition is kept in abeyance due to insufficient funds and no interest showing by the State Govt.

(July 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
196	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 1,339.48	4,190.00	88.56	12/2015 -	03/2020	51	212.81	Delay in land acquisition affected work progress in Rongchong and Kalimpong (West Bengal).
197	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00 -	2,973.42	10.44	03/2015 03/2020	03/2020	60	249.81	Land acquisition is pending.
	Total		31,140.62 -	88,821.64	40,201.58					
	ROAD TRANSPORT AND HIGHWAYS									
198	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	624.00	-	04/2014 -	07/2015	15	0	
199	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	909.00	982.90	05/2014 -	07/2015	14	0	
200	GUWAHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	175.96	-	04/2008 08/2015	08/2015	88	0	
201	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	-	06/2008 08/2015	08/2015	86	0	
202	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	201.66	191.80	09/2008 -	09/2015	84	30.1	
203	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	398.00	344.40	02/2014 -	09/2015	19	0	Project abandoned by contractor
204	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	-	05/2008 10/2015	10/2015	89	0	
205	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	2,388.00	2,301.00	06/2014 -	11/2015	17	0	
206	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	280.13	173.80	11/2008 -	12/2015	85	80.68	
207	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	198.16	242.40	04/2008 12/2015	12/2015	92	0	
208	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	209.00	11.28	01/2013 -	12/2015	35	0	Land acquisition Forest clearance Poor progress by the contractor
209	SONAPUR TO GUWAHATI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	245.00	-	03/2008 01/2016	01/2016	94	0	
210	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	208.00	-	04/2008 01/2016	01/2016	93	0	

(July 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
211	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, ASSAM	12/2003	217.61 309.56	309.56	-	04/2010 01/2016	01/2016	69	42.25	
212	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI, MULTI STATE	02/2013	1,232.00 -	1,232.00	590.90	08/2015 -	02/2016	6	0	
213	SIX LANING OF CHANDIKHOL- JAGATPUR-BHUBANESWAR - [N24000205]NHAI, MULTI STATE	12/2011	1,047.00 -	1,047.00	295.70	06/2014 -	03/2016	21	0	
214	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI, MAHARASHTRA	04/2012	484.19 -	484.19	285.50	10/2014 -	03/2016	17	0	
215	PANIKHOLI-RIMOLI - [N24000197]NHAI, ODISHA	03/2012	1,410.00 -	1,410.00	929.60	09/2014 -	06/2016	21	0	
216	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI, MULTI STATE	02/2009	1,693.75 -	1,693.75	2,762.00	08/2011 -	09/2016	61	0	
217	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI, ODISHA	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2016	35	0	
218	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI, MULTI STATE	09/2011	2,848.00 -	2,848.00	1,138.00	03/2014 -	04/2017	37	0	
	Total		15,568.71 -	15,832.41	10,486.88					
	<u>SHIPPING AND PORTS</u>									
219	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU, MAHARASHTRA	01/2007	366.39 669.46	669.46	407.32	12/2010 -	01/2016	61	82.72	
	Total		366.39 -	669.46	407.32					
	<u>TELECOMMUNICATIONS</u>									
220	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL, MULTI STATE	10/2009	384.00 -	384.00	66.02	10/2010 08/2015	09/2015	59	0	
	Total		384.00 -	384.00	66.02					
	<u>URBAN DEVELOPMENT</u>									
221	FARIDABAD EXTENSION - [N28000057]DMRCL, DELHI	09/2011	2,494.00 -	2,494.00	1,272.44	09/2014 -	08/2015	11	0	CMRS inspection is to be done shortly for giving statutory clearances for starting the commercial operation of line. Mandatory clearances are being perused.

(July 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
222	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD,ODISHA	11/2012	238.43 -	238.43	-	02/2015 -	08/2015	6	0	Finalization of flooring work in 1st year lab building and approval of sample flat for Grade- A qtr from client awaited.
223	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 -	315.00	3.11	06/2015 -	08/2015	2	0	
224	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	-	11/2014 -	10/2015	11	0	
225	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85 -	261.85	6.26	05/2013 -	11/2015	30	0	Initial delay of 1 year in availability of site, subsequent delay due to non-uniform flow of funds during 2012-13 & 2013-14, delay in finalization of interior scheme, non-availability of full site till date, non-performance of Interior Agency
226	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	12/2015	11	0	
227	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI	05/2012	405.01 -	405.01	-	12/2014 -	04/2016	16	0	Extra time involved in finalization of tender for addressing certain issues of client department.
228	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	-	03/2016 -	05/2016	2	0	
229	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 14,600.00	14,600.00	10,826.56	12/2015 -	08/2016	8	0	
230	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	38,585.00	16,432.68	03/2016 -	12/2016	9	0	
231	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	188.87	5.79	12/2014 -	12/2016	24	0	

(July 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
232	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD, WEST BENGAL	02/2014	156.57 -	156.57	-	09/2015 -	12/2016	15	0	
233	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD, DELHI	07/2012	884.30 -	884.30	-	08/2014 -	06/2017	34	0	The work was terminated on 24-07-2014 because of the non performance of the contractor for the first package. However, the tender for balance items of the package I along with package III has been awarded and work started at site.
	Total		81,707.72 -	81,707.72	28,546.84					
	Grand Total		492,382.24	601,985.63	351,503.01					

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(July 2015)

Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Date of Commissioning (Month/Year)		Cost Overruns (%)	T.O.R.s (in months)
					Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	09/2016	62.57	72
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	12/2008 -	10/2015	31.12	82
	Total		16,663.00 -	22,947.00				
	<u>CIVIL AVIATION</u>							
3	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]	10/2012	217.60 -	244.10	03/2015 -	09/2015	12.18	6
4	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]	02/2011	452.00 -	489.00	03/2015 -	07/2015	8.19	4
	Total		669.60 -	733.10				
	<u>COAL</u>							
5	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	03/2016	478.50	36
6	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	479.63	03/2013 -	03/2017	0.02	48
7	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,583.77	06/2009 -	07/2015	76.47	73
8	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,602.74	03/2012 -	08/2015	34.63	41
	Total		7,627.19 -	11,894.53				
	<u>HEAVY INDUSTRY</u>							
9	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78	75
	Total		1,718.00 -	3,827.30				
	<u>PETROCHEMICALS</u>							
10	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	9,833.52	04/2012 -	09/2015	80.08	41
	Total		5,460.61 -	9,833.52				

(July 2015)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	PETROLEUM							
11	MARKETING TERMINAL AT PARADEEP - [N16000168]	07/2009	199.75 -	239.73	07/2013 -	10/2015	20.02	27
12	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79	10/2014 -	10/2016	49.38	24
13	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) [N16000146]	02/2012	666.00 -	838.08	11/2015 -	11/2016	25.84	12
14	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE [N16000157]	01/2006	732.00 -	1,227.00	10/2011 -	01/2016	67.62	51
15	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79 -	1,256.72	05/2013 -	12/2015	45.83	31
16	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	06/2016	37.72	15
17	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	01/2016	70.49	48
18	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	05/2016	29.42	14
19	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]	12/2012	3,513.07 -	4,619.94	02/2016 -	12/2017	31.51	22
20	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00 -	34,555.00	11/2012 -	10/2015	16.05	35
	Total		39,983.40 -	48,757.91				
	POWER							
21	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	346.79	08/2014 -	12/2015	16.63	16
22	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	07/1998	368.72 -	1,381.71	07/2006 02/2015	10/2016	274.73	123
23	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	1,007.68	07/2013 -	08/2015	139.35	25
24	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	721.81	09/2010 -	03/2016	51.10	66
25	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,487.49	08/2013 -	03/2016	159.15	31
26	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]	09/2005	1,061.38 -	1,929.15	09/2009 -	06/2016	81.76	81
27	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	07/2010 -	05/2018	79.77	94
28	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]	12/2011	1,746.65 -	2,228.71	08/2014 -	03/2016	27.60	19
29	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,159.07	09/2008 -	03/2016	21.34	90

(July 2015)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
30	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087	09/2010	2,074.86 -	2,348.37	03/2013 -	10/2015	13.18	31
31	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT [N18000042	08/2008	2,491.58 -	3,745.08	06/2013 -	12/2019	50.31	78
32	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239	12/2004	2,496.90 -	6,476.34	12/2009 06/2016	03/2017	159.38	87
33	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C [N18000096	03/2011	2,569.25 -	3,105.51	03/2014 -	08/2015	20.87	17
34	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014	11/2006	2,978.48 -	3,846.30	03/2013 -	12/2018	29.14	69
35	KISHANGANGA HEP (3X110 MW) - [N18000031	01/2009	3,642.04 -	5,497.72	01/2016 -	11/2016	50.95	10
36	PARBATI HEP (4X200 MW) (NHPC) II - [180100210	09/2002	3,919.59 -	7,818.68	09/2009 -	12/2018	99.48	111
37	BONGAIGAON THERMAL POWER PROJECT - [N18000041	01/2008	4,375.35 -	6,749.18	09/2011 -	03/2017	54.25	66
38	BARH STPP(3X660MW) NTPC - [180100242	02/2005	8,692.97 -	15,095.67	01/2011 -	03/2018	73.65	86
	Total		41,624.08 -	68,924.12				
	<u>RAILWAYS</u>							
39	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	2,371.85	03/2005 12/2008	12/2019	2,019.62	177
40	ETAWAH-MAINPURI (NL),NCR - [220100318	04/1997	120.00 -	245.39	12/2008 -	10/2015	104.49	82
41	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION [N22000162	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44	21
42	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094	02/2008	171.10 -	275.08	03/2012 -	03/2016	60.77	48
43	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	335.00	06/2004 -	12/2015	72.62	138
44	KATAKHAL TO BHARABI - [N22000126	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41	39
45	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097	03/1984	293.97 -	1,428.00	06/2005 -	12/2019	385.76	174
46	DANGOAPOLI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164	04/2010	309.44 -	583.00	12/2015 -	03/2016	88.40	3
47	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	04/2006	325.00 -	1,564.54	03/2010 -	03/2017	381.40	84
48	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,544.40	03/1998 -	12/2019	299.79	261
49	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107	04/2007	482.00 -	874.57	03/2013 -	09/2015	81.45	30

(July 2015)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
50	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	492.98 -	1,727.27	12/2010 -	03/2018	250.37	87
51	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	1,781.98	03/2004 -	03/2016	259.68	144
52	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	619.34 -	2,820.25	04/2014 -	03/2018	355.36	47
53	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76	98
54	BHOPAL BINA 3D LINE DOUBLING - [N22000077	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41	69
55	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	6,570.75	03/2011 -	03/2019	803.12	96
56	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	2,531.34	12/2008 -	03/2018	245.34	111
57	AGARTALA SABROOM, NL, NEFR - [N22000099	04/2008	813.34 -	2,876.00	03/2014 -	03/2018	253.60	48
58	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124	04/2006	850.00 -	2,973.42	03/2015 -	03/2020	249.81	60
59	CONSTRUCTION OF NL FROM KUMARGHAT- AGARTALA [N22000194	04/1999	895.00 -	1,242.25	03/2007 -	03/2016	38.80	108
60	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	03/2009 -	10/2015	156.57	79
61	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	4,190.00	12/2015 -	03/2020	212.81	51
62	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	06/2017	233.08	110
63	LUMDING-SILCHAR JIRIBAM, BADARPUR- BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127	04/1996	1,676.31 -	5,500.00	03/2009 -	03/2016	228.10	84
64	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60	193
65	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68	60
	Total		22,946.70 -	80,627.72				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
66	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH- 25, KM.75-80.06 [240106221	12/2003	155.00 -	201.66	09/2008 -	09/2015	30.10	84
67	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	11/2008 -	12/2015	80.68	85
68	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063	12/2003	217.61 -	309.56	04/2010 -	01/2016	42.25	69
	Total		527.65 -	791.35				

(July 2015)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>SHIPPING AND PORTS</u>							
69	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	01/2007	366.39 -	669.46	12/2010 -	01/2016	82.72	61
	Total		366.39 -	669.46				
	Grand Total		137,586.62	249,006.01				

Details of Projects Without Date of Commissioning

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>CIVIL AVIATION</u>				
1	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 -	05/2012 -	03/2015
2	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	03/2014 -	05/2015
3	GAGAN PROJECT - [N04000065]AAI,MULTI STATE	09/2008	626.00 -	06/2013 -	-
	Total		1,305.89 -		
	<u>COAL</u>				
4	JALLARAM SHAFT PROJECT - [N06000025]SCCL,TELANGANA	09/2007	467.78 -	03/2013 -	-
5	BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH	09/2008	203.82 -	03/2015 -	03/2015
	Total		671.60 -		
	<u>STEEL</u>				
6	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]NMDC,CHHATISGARH	01/2007	607.17 -	12/2011 01/2015	03/2015
7	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL,ANDHRA PRADESH	10/2005	8,692.00 12,291.00	10/2009 10/2012	04/2015
8	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH	04/2014	188.93 -	04/2015 -	04/2015
9	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,KARNATAKA	04/2011	572.00 -	04/2013 09/2014	06/2015
	Total		10,060.10 -		
	<u>PETROLEUM</u>				
10	DEVELOPMENT OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,MULTI STATE	04/2003	429.82 3,955.21	04/2006 06/2012	06/2015
11	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]ONGC,TRIPURA	07/2008	288.04 253.66	08/2012 06/2015	06/2015
12	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC,MULTI STATE	11/2010	331.20 -	08/2013 06/2015	06/2015
13	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00 -	12/2012 -	06/2015
14	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]JPRL,ANDHRA PRADESH	01/2006	672.00 1,178.35	10/2011 -	06/2015
15	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	- -	-
16	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
17	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 -	- -	-
18	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00 -	- -	-
19	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE	02/2015	890.00 -	- -	-
20	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 188.89	01/2014 -	-
	Total		10,755.83 -		
	<u>POWER</u>				
21	BARH STPP STAGE -II - [N18000047]NTPC,BIHAR	02/2008	7,341.04 10,852.46	10/2013 -	03/2015
22	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]NEEPCO, TRIPURA	07/2012	296.87 363.73	12/2014 -	05/2015
23	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-
24	SYSTEM STRENGTHENING -XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	06/2012 -	-
25	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,ANDHRA PRADESH	03/2012	206.44 -	06/2014 -	-
	Total		14,362.02 -		
	<u>RAILWAYS</u>				
26	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	07/2008
27	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87 -	- 03/2010	03/2010
28	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	02/2012
29	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 663.01	06/1999 -	07/2012
30	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 03/2012	12/2012
31	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	06/2013 06/2013	06/2013
32	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	611.03 -	12/2011 11/2013	11/2013
33	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 -	- -	02/2014
34	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2014
35	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	02/2009 02/2009	08/2014
36	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	03/2009 03/2009	08/2014

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
37	CUTTACK - BARANG (LD) - [220100326]RVNL, ODISHA	04/1995	127.13 -	- 10/2014	10/2014
38	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER, WEST BENGAL	04/2010	171.02 -	06/2013 -	01/2015
39	PANVEL PEN DOUBLING - [N22000255]CR, MULTI STATE	04/2006	96.16 -	- -	01/2015
40	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR, MULTI STATE	04/1986	158.77 608.02	03/1994 -	03/2015
41	NANDYAL-YERRAGUNTALA(NL), SCR - [220100192]SCR, ANDHRA PRADESH	03/1996	155.74 164.36	02/2009 -	03/2015
42	MUNEERABAD-MAHABOBNAGAR(NL), SCR - [220100205]SCR, MULTI STATE	04/1997	218.24 236.41	- -	03/2015
43	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, WEST BENGAL	04/1974	393.46 393.46	03/2007 03/2007	03/2015
44	GULBARGA-BIDAR, SCR(NL) - [220100254]SCR, KARNATAKA	02/1998	242.42 369.70	- 05/2009	03/2015
45	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR, RAJASTHAN	04/2008	829.74 -	03/2015 -	03/2015
46	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR, TAMIL NADU	04/2007	247.00 -	- -	03/2015
47	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER, MULTI STATE	04/2011	248.07 -	03/2015 -	03/2015
48	PEN ROHA DOUBLING - [N22000254]CR, MULTI STATE	04/2007	98.74 -	- -	03/2015
49	DELANG-PURI DOUBLING - [N22000320]ECOR, ODISHA	03/2011	165.16 -	03/2015 -	03/2015
50	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR, UTTAR PRADESH	04/1999	108.00 427.21	12/2009 03/2011	06/2015
51	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL - [220100149]RVNL, CHHATISGARH	04/1995	304.00 -	12/2012 -	-
52	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, ODISHA	04/1996	301.64 -	- 09/2009	-
53	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA	04/1998	183.23 -	02/2015 -	-
54	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL, ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-
55	GOELKERA-MANOHARPUR, (LD)(SER) - [N22000045]SER, JHARKHAND	03/1997	261.70 -	02/2006 -	-
56	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-
57	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL, CHHATISGARH	09/2006	324.90 -	03/2010 -	-
58	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	-
59	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL, ANDHRA PRADESH	03/2012	1,503.71 -	- -	-
60	VIRAMGAM-BHILDI(WR), GC - [220100062]WR, MULTI STATE	04/1990	155.66 -	- 03/2010	-
61	MANDARHILL-DUMKA-RAMPURHAT (NL), ER - [220100168]ER, JHARKHAND	04/1995	900.05 -	12/2011 12/2010	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
62	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	- -	-
63	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 -	- -	-
64	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	- -	-
65	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-
66	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-
67	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	- -	-
68	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	2,957.21 -	07/2005 -	-
69	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	05/2008 -	-
70	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 501.69	03/2012 -	-
71	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	- -	-
72	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-
73	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-
74	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 -	- -	-
75	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE	03/1998	280.00 -	- -	-
76	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	- -	-
77	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 3,385.14	12/2006 -	-
78	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	02/2011 02/2011	-
79	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	- 12/2009	-
80	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-
81	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 -	- -	-
82	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	- -	-
83	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-
84	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-
85	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-
86	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
87	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	- -	-
88	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	- -	-
89	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	- -	-
90	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 332.92	03/2012 -	-
91	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	378.56 -	- -	-
92	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	- -	-
93	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE	12/2006	170.00 -	03/2011 -	-
94	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 -	- -	-
95	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 -	- -	-
96	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	1,106.62 -	12/2010 -	-
97	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	03/2014 -	-
98	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 732.06	03/2014 -	-
99	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	-
100	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER,WEST BENGAL	04/2009	533.38 -	12/2011 -	-
101	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER,WEST BENGAL	04/2004	293.74 -	12/2010 -	-
102	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-
103	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	03/2013 -	-
104	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	03/2014 -	-
105	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	-
106	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-
107	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
108	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	-
109	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	-
110	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	- -	-
111	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	- -	-
112	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
113	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	- -	-
114	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-
115	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	- -	-
116	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	- -	-
117	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	- -	-
118	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-
119	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 913.48	- -	-
120	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT	04/2013	1,266.89 -	- -	-
121	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	- -	-
122	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	- -	-
123	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-
124	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	-
125	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
126	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
127	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	- -	-
128	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	- -	-
129	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	- -	-
130	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	- -	-
131	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	- -	-
132	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	- -	-
133	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- -	-
134	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	- -	-
135	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	- -	-
136	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-
137	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
138	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-
139	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-
140	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-
141	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-
142	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-
143	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-
144	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-
145	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-
146	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-
147	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-
148	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
149	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-
150	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-
151	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-
152	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	- -	-
153	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-
154	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
155	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-
156	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-
157	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	- -	-
158	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-
159	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
160	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
161	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-
162	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
163	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-
164	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-
165	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-
166	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	- -	-
167	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-
168	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-
169	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-
170	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-
171	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-
172	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-
173	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-
174	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-
175	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-
176	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRACHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-
177	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-
178	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-
179	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	- -	-
180	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-
181	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-
182	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-
183	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-
184	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-
185	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
186	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-
187	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-
188	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-
189	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-
190	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	- -	-
191	SANTOSHAPUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-
192	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-
193	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-
194	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-
195	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-
196	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	- -	-
197	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-
198	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE	04/2013	723.00 -	- -	-
199	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 -	- -	-
200	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE	04/2008	184.26 -	- -	-
201	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-
202	GUDUR-DURGARAJPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-
203	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-
204	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-
205	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-
206	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-
207	DELHI-SOHNANU-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-
208	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-
209	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
210	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-
211	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	-
212	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-
213	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-
214	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	- -	-
215	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-
216	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-
217	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
218	MUDKHED-PARBHANI - [N22000283]SCR,MAHARASHTRA	04/2011	390.60 -	- -	-
219	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	- -	-
220	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49 -	- -	-
221	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	- -	-
222	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
223	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-
224	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-
225	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-
226	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-
227	UNCHAHAH-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-
228	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-
229	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-
230	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	- -	-
231	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-
232	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	- -	-
233	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	-
234	MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-
235	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
236	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	01/1999 -	-
237	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 -	-
238	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-
239	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	01/1999 -	-
240	MM FROM PANSKURA-GHATAL NL - [N22000309]SER, WEST BENGAL	04/2011	276.69 -	01/1999 -	-
241	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 -	- -	-
242	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 -	- -	-
243	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	- -	-
244	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-
245	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR,TAMIL NADU	04/2011	190.10 -	- -	-
246	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,900.00 -	- -	-
247	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	- -	-
248	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 -	- -	-
249	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	- -	-
250	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-
251	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-
252	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA	05/2015	400.00 -	- -	-
253	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA	03/2015	960.00 -	- -	-
254	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 -	- -	-
255	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	720.00 -	- -	-
	Total		112,281.52 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
256	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,MULTI STATE	12/2012	1,479.00 -	06/2015 -	06/2015
257	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA	02/2010	390.56 -	02/2012 -	06/2013
258	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	02/2014 -	02/2014
259	2LANING WITH PS GOPALGANJ-CHAPPRA - [N24000190]NHAI,BIHAR	12/2011	325.00 -	05/2014 -	05/2014

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
260	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,KARNATAKA	11/2010	680.00 -	- -	07/2014
261	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00 -	10/2014 -	10/2014
262	RAJMARG CHORAH TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	10/2008 -	01/2015
263	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 157.47	09/2007 03/2014	03/2015
264	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	04/2015 -	04/2015
265	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	05/2015
266	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	01/2013 -	05/2015
267	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	06/2005 -	-
268	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	10/2008 -	-
269	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	-
270	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	-
271	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	-
272	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	04/2009 -	-
273	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	06/2008 -	-
274	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	06/2008 -	-
275	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	09/2008 -	-
276	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	10/2008 -	-
277	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	07/2008 -	-
278	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-
279	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	06/2008 -	-
280	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 -	09/2007 -	-
281	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	-
282	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	02/2010 -	-
283	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-
284	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	09/2007 -	-
285	NH CONNECTIVITY TO ICTT VALLARPADA NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	02/2010 -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
286	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	09/2010 -	-
287	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	-
288	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	07/2012 -	-
289	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	09/2012 -	-
290	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	05/2012 -	-
291	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	10/2011 -	-
292	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	10/2011 -	-
293	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	-
294	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	12/2012 -	-
295	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	-
296	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	- -	-
297	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	09/2013 -	-
298	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	-
299	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	03/2013 -	-
300	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	-
301	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	07/2013 -	-
302	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	-
303	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	11/2012 -	-
304	DEVIHALLI-HASSAN - [N24000152]NHAI,KARNATAKA	12/2010	453.00 -	- -	-
305	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	09/2013 -	-
306	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	06/2013 -	-
307	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-
308	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	-
309	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,KARNATAKA	12/2010	480.00 -	- -	-
310	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-
311	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
312	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-
313	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	-
314	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	-
315	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT	12/2010	1,008.50 -	06/2013 -	-
316	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,GUJARAT	03/2011	785.50 -	08/2013 -	-
317	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	-
318	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-
319	SIX LANNING OF HOSUR- KRISHNAGIRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	12/2013 -	-
320	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	-
321	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	-
322	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	-
323	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	-
324	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	-
325	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-
326	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	03/2013 -	-
327	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	01/2014 -	-
328	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	-
329	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	02/2014 -	-
330	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	-
331	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-
332	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	-
333	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	-
334	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	-
335	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	01/2014 -	-
336	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	08/2013 -	-
337	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	02/2013 -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
338	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	-
339	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	-
340	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	08/2013 -	-
341	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	08/2013 -	-
342	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	08/2013 -	-
343	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	09/2014 -	-
344	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	07/2012 -	-
345	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	-
346	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL	02/2012	702.16 -	07/2014 -	-
347	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI, BIHAR	07/2012	356.40 -	07/2014 -	-
348	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	10/2013 -	-
349	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	10/2013 -	-
350	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	06/2014 -	-
351	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH	10/2012	250.50 -	10/2014 -	-
352	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	07/2014 -	-
353	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT	03/2012	828.00 -	09/2014 -	-
354	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN	03/2012	333.51 -	09/2014 -	-
355	BARSAT-KRISHNANAGAR - [N24000229]NHAI, WEST BENGAL	08/2012	867.00 -	02/2015 -	-
356	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	02/2014 -	-
357	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI,ANDHRA PRADESH	09/2013	606.00 -	- -	-
358	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI,TELANGANA	04/2014	1,123.17 -	- -	-
	Total		71,750.36 -		
	SHIPPING AND PORTS				
359	ACQUISITION OF TWO (2) NOS OF 317000 DWT VLCC'S FROM JIANGSU RONGSHENG HEAVY INDUSTRIES CO.LTD.,CHIN - [N25000064]SHIPP.,MAHARASHTRA	10/2010	994.82 -	11/2013 -	11/2013
360	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 -	04/2009 -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
361	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-
362	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 -	12/2010 -	-
363	MODIFICATION AND STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST,GUJARAT	06/2010	277.00 -	03/2012 -	-
	Total		5,172.89 -		
	<u>URBAN DEVELOPMENT</u>				
364	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI - [N28000064]CPWD,DELHI	01/2010	162.90 -	07/2012 -	06/2014
365	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA - [N28000078]CPWD,BIHAR	11/2006	2,727.89 -	03/2010 -	10/2014
366	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 -	11/2014 -	12/2014
367	CONSTRUCTION OF MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB - [N28000070]CPWD,PUNJAB	08/2005	191.24 -	08/2007 -	03/2015
368	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	03/2012 -	04/2015
369	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD,WEST BENGAL	01/2009	225.81 -	06/2012 -	05/2015
370	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA	05/2006	6,395.00 -	06/2011 -	-
371	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]CPWD,BIHAR	02/2012	171.10 -	09/2014 -	-
372	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	10/2012 -	-
373	REHABILITATION AND STRENGTHENING OF SEWEWAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI(IN ZONE 2 IN - [N28000082]JnNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-
	Total		10,732.40 -		
	Grand Total		237,092.61		

Details of Projects Without Original Date of Commissioning

(July 2015)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>CIVIL AVIATION</u>								
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, ANDAMAN & NICOBAR ISLANDS	10/2013	314.61	314.61	17.82	- 09/2018	09/2018	0(R3)	0/0
	Total		314.61	314.61	17.82				0/0
	<u>RAILWAYS</u>								
2	HOSADURGA - CHICKJAJUR (28.89 KM) - [N22000324]SWR, KARNATAKA	04/2010	203.40	203.40	153.29	- -	09/2015	-	0/0
3	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER, MULTI STATE	04/1999	744.71	744.71	576.86	- -	03/2016	-	0/1
4	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR, TAMIL NADU	09/2006	343.17	914.98	846.18	- -	03/2016	-	0/0
5	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]EOR, ODISHA	03/2012	155.81	155.81	18.25	- -	12/2016	-	0/0
6	RAMGANJ-MUNDI-BHOPAL (NL), WCR - [220100314]WCR, MADHYA PRADESH	04/2001	470.92 727.13	1,225.90	257.59	- -	03/2017	-	0/0
7	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, MADHYA PRADESH	04/2005	383.79 663.67	1,101.16	194.91	- -	03/2017	-	0/0
8	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	200.00 200.00	496.24	213.72	- -	03/2017	-	0/0
9	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR, MULTI STATE	04/2010	241.52 210.00	394.28	233.46	- -	03/2017	-	0/0
10	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER, JHARKHAND	04/2012	258.20 315.13	365.00	2.52	- -	12/2017	-	0/0
11	KANPUR-KASGANJ-MATHURA(GC), NER - [220100197]NER, UTTAR PRADESH	03/1997	677.97 1,062.36	1,651.54	1,621.40	- -	03/2018	-	0/0
12	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR, BIHAR	04/2008	282.92 282.92	565.13	2.80	- 03/2014	03/2018	48(R3)	0/0
13	AGARTALA-AKHAURA NL - [N22000195]NFR, TRIPURA	04/2012	252.00	886.65	-	- -	03/2018	-	0/0
14	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR, WEST BENGAL	04/2011	209.77 190.39	441.45	85.78	- -	03/2018	-	0/0
15	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR, WEST BENGAL	04/2012	283.55 278.21	288.81	11.74	- -	03/2018	-	0/0
16	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR, MULTI STATE	04/2010	242.22 171.00	679.57	40.41	- -	03/2018	-	0/0
17	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR, MULTI STATE	04/2011	165.82 165.82	435.58	0.56	- -	03/2018	-	0/0

(July 2015)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
18	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NFR,MULTI STATE	04/1999	523.17 380.60	1,653.55	1,040.11	- -	03/2018	-	0/0
19	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	312.12 257.93	453.10	134.79	- -	03/2018	-	0/0
20	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 -	1,143.60	189.12	- -	03/2018	-	0/0
21	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR, WEST BENGAL	04/1983	36.80 36.38	1,336.57	255.55	- -	03/2019	-	0/0
22	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	300.00 300.00	827.73	53.52	- -	03/2019	-	0/0
23	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 1,798.00	1,887.90	-	- -	03/2019	-	0/0
24	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 205.31	563.13	22.39	- -	03/2019	-	0/0
25	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM	04/2012	246.07 246.07	364.06	0.30	- -	03/2019	-	0/0
26	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 651.17	1,009.00	7.50	- -	12/2019	-	0/0
27	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	4,487.70	-	- -	03/2020	-	0/0
28	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	4,083.02 -	5,307.90	7.79	- 03/2016	03/2020	48(R3)	0/0
	Total		18,290.57 -	29,584.45	5,970.54				0/1
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
29	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,KARNATAKA	09/2010	671.00 -	671.00	1,273.00	- -	12/2015	-	2/3
	Total		671.00 -	671.00	1,273.00				2/3
	Grand Total		19,276.18	30,570.06	7,261.36				2/4

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	05/2018	12320	17
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	10/2017	11459	22
3	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	10/2015	13171	82
4	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	09/2016	3492	72

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
5	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	AAI	10/2012	03/2015	09/2015	217.6	6
6	CONSTRUCTION OF NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT	AAI	01/2009	01/2011	09/2017	309.46	80

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
7	KALYANIKHANI OPENCAST PROJECT	SCCL	07/2012	07/2016	03/2017	417.33	8
8	RCE OF INDARAM OCP (1.20 MTPA)	SCCL	07/2011	03/2015	03/2019	162.76	48
9	JALAGAM VENGALA RAO OCP-II	SCCL	07/2011	03/2015	03/2018	447.06	36
10	RG OC -III EXTENSION (PHASE -II) PROJECT	SCCL	06/2012	06/2015	03/2016	365.01	9
11	TUTICORIN THERMAL POWER PROJECT-2X500 MW	NLC	05/2008	03/2012	08/2015	4904.54	41
12	MOONIDIH XV SEAM UG	BCCL	08/2011	04/2015	04/2019	1230.27	48
13	GOPAL PRASAD OCP (15MTY)	MCL	02/2008	03/2015	03/2021	395.87	72
14	TALABIRA OCP	MCL	03/2008	03/2016	03/2020	447.72	48
15	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	03/2012	03/2017	207.28	60
16	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2017	479.53	48
17	RKP OCP PHASE-I	SCCL	03/2010	03/2015	03/2016	209.78	12
18	BALRAM OCP EXTENSION, MCL 8.00 MTY	MCL	12/2007	03/2010	03/2017	172.08	84
19	GEVRA EXPANSION OCP (SECL) (25-35) MTY	SECL	06/2010	03/2014	03/2016	2675.67	24
20	DIPKA EXPANSION OCP (SECL) (20-25) MTY	SECL	12/2009	03/2014	03/2016	1943.66	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
21	MURAI DIH UG TURN-KEY PROJECT	BCCL	02/2011	04/2014	03/2016	339.88	23
22	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2018	249.03	72
23	JHANJRA R-VI SEAM PSLW	ECL	11/2006	03/2011	03/2017	287.18	72
24	RAJMAHAL OC EXP.	ECL	09/2009	03/2014	03/2016	153.82	24
25	KAKATIYA LONGWALL	SCCL	12/2008	12/2012	03/2017	453.63	51
26	KISTARAM OCP	SCCL	11/2010	03/2015	03/2018	242.29	36
27	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2020	178.44	72
28	MANUGURU OC-II EXTENSION PHASE-II	SCCL	03/2010	03/2012	03/2016	181.19	48
29	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	NLC	10/2004	06/2009	07/2015	2030.78	73
30	WIND POWER PROJECT, KAZHUNEERKULAM, TAMILNADU	NLC	04/2012	10/2014	08/2015	364.75	10
31	KRISHNASHILA (NCL) (4MTY)	NCL	06/2011	03/2013	03/2016	789.88	36
32	ASHOK EXPN OCP CCL (10 MTY)	CCL	12/2007	03/2011	03/2017	341.63	72
33	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	03/2017	259.4	60
34	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2016	418.97	48
35	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2016	163.51	60
36	PURNADIH OCP (3.0 MTY)	CCL	07/2008	03/2013	03/2016	210.98	36
37	NORTH URIMARI OCP (3.0 MTY)	CCL	12/2007	03/2012	03/2017	179.87	60
38	TAPIN OCP (2.5 MTY)	CCL	08/2008	03/2012	03/2016	264.68	48
39	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2017	162.46	36
40	ADRIYALA SHAFT PROJECT	SCCL	12/2009	03/2013	03/2016	212.34	36
41	MADHUBAND NLW WASHERY	BCCL	08/2010	05/2014	10/2016	289.45	29
42	PATHERDIH NLW WASHERY	BCCL	10/2012	04/2014	11/2016	269.82	31
43	KULDA OCP (MAHANADI COALFIELDS LTD)	MCL	01/2005	03/2010	03/2016	302.96	72

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
44	CHURCHA ROUG (1.35MTY)	SECL	06/2008	03/2014	03/2016	462.35	24
45	KANIHA OCP, MCL, (10.0 MTY)	MCL	12/2007	03/2013	03/2017	457.77	48
46	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2009	03/2014	03/2016	321.5	24
47	BLOCK-B OCP NCL (3.5 MTY)	NCL	06/2011	03/2015	03/2016	746.04	12
48	JAGANNATHPOR OCP (3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	60
49	MAGADH OC 20 MTY (CCL)	CCL	08/2008	07/2012	03/2016	706.4	44
50	NEYVELI NEW THERMAL POWER PROJECT (2X500 MW)	NLC	06/2011	12/2015	04/2018	5907.11	28

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
51	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	HIPE	04/2011	09/2011	12/2017	1718	75

PETROCHEMICALS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
52	ASSAM GAS CRACKER PROJECT	BCPL	04/2006	04/2012	09/2015	5460.61	41

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
53	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	06/2016	871.35	15
54	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	ISPRL	01/2006	10/2011	01/2016	732	51
55	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	11/2016	666	12
56	IOR OF B-173A FIELD	ONGC	01/2012	03/2014	05/2016	352.49	26
57	DEVELOPMENT OF C-26 CLUSTER FIELDS	ONGC	03/2012	05/2014	05/2016	2592.17	24
58	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV)	ONGC	01/2010	03/2013	06/2016	723.64	39
59	AHMEDABAD REDEVELOPMENT PROJECT	ONGC	11/2010	12/2014	12/2017	1916.1	36
60	INTEGRATED DEVELOPMENT OF BASSEIN FIELD	ONGC	12/2012	02/2016	12/2017	3513.07	22
61	RECONSTRUCTION OF BPA AND BPB	ONGC	03/2013	04/2015	12/2015	1138.5	8

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
	PLATFORMS						
62	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS (OSV)	ONGC	06/2007	09/2011	12/2015	736.65	51
63	DEVELOPMENT OF WO-16 CLUSTER FIELDS	ONGC	06/2010	01/2014	12/2015	2523	23
64	ANKLESWAR REDEVELOPMENT	ONGC	11/2010	12/2014	12/2018	2189.63	48
65	MEHESANA REDEVELOPMENT PROJECT	ONGC	11/2010	04/2015	12/2017	3823	32
66	102 MW WIND POWER PROJECT	ONGC	07/2010	06/2012	09/2015	1106	39
67	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG	OIL	04/2010	06/2012	11/2015	270	41
68	MARKETING TERMINAL AT PARADEEP	IOCL	07/2009	07/2013	10/2015	199.75	27
69	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	01/2016	993	48
70	LPG TERMINAL AT KOCHI	IOCL	12/2012	01/2016	04/2017	607.06	15
71	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	12/2017	4124.35	20
72	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE	ONGC	04/2013	04/2015	05/2017	284.82	25
73	RESID UPGRADATION PROJECT	CPCL	02/2011	11/2015	07/2016	3110.36	8
74	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND)	IOCL	04/2011	05/2015	12/2015	191.96	7
75	DAMAN DEVELOPMENT PROJECT	ONGC	08/2014	05/2019	03/2020	6086.08	10
76	CONSTRUCTION OF 6 ETPS	ONGC	03/2009	09/2012	12/2015	317.64	39
77	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I	GAIL	07/2009	01/2013	12/2018	3957	71
78	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	12/2015	861.79	31
79	PARADIP-RAIPUR- RANCHI PIPELINE	IOCL	08/2009	09/2012	03/2016	1793	42
80	PARADIP REFINERY PROJECT	IOCL	02/2009	11/2012	10/2015	29777	35
81	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH)	GAIL	12/2009	06/2011	03/2016	463.32	57
82	ASSAM RENEWAL PROJECT FOR GROUP A	ONGC	03/2009	03/2013	03/2017	2465.15	48
83	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1)	ONGC	10/2013	10/2014	10/2015	429.06	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
84	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	05/2016	2059.63	14
85	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD	ONGC	04/2012	12/2014	05/2016	600.17	17
86	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY	BPCL	03/2012	12/2014	08/2015	1419	8
87	PARADIP HALDIA DURGAPUR LPG PIPELINE	IOCL	02/2011	08/2015	06/2016	913	10
88	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	10/2016	309.81	24
89	MOUNDED BULLET PROJECT AT CPCL	CPCL	12/2012	12/2014	09/2015	279	9

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
90	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI	PGCIL	06/2012	06/2015	08/2016	1909.24	14
91	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B	PGCIL	03/2013	12/2015	06/2016	2514.88	6
92	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH	PGCIL	05/2011	05/2014	06/2016	1961.87	25
93	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2018	2978.48	69
94	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	03/2017	4375.35	66
95	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2019	2491.58	78
96	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2	PGCIL	12/2011	08/2014	09/2015	2422.66	13
97	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	03/2017	2496.9	87
98	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1	PGCIL	10/2011	11/2013	12/2015	558.26	25
99	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER (MADRAS) LIMITED L	PGCIL	09/2011	09/2014	06/2016	1940.13	21
100	TEHRI PUMPED STORAGE PLANT (1000MW)	THDCIL	07/2006	07/2010	05/2018	1657	94
101	SYTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	11/2015	487.49	17
102	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH	PGCIL	11/2011	07/2014	03/2016	2127.51	20
103	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	03/2016	573.99	31
104	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL)	PGCIL	03/2005	12/2007	12/2015	1007.16	96
105	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2018	3919.59	111

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
106	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	NHPC	09/2005	09/2009	06/2016	1061.38	81
107	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	03/2016	477.69	66
108	NORTHERN REGION SYSTEM STRENGHTENING SCHEME-XIX	PGCIL	02/2009	02/2012	03/2016	410.29	49
109	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	03/2016	4824.12	41
110	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI	PGCIL	08/2010	04/2013	03/2016	1677.57	35
111	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME	PGCIL	03/2010	11/2012	03/2016	965.58	40
112	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C	PGCIL	03/2011	03/2014	08/2015	2569.25	17
113	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B	PGCIL	03/2011	11/2013	12/2015	1585.12	25
114	NORTHERN REGION SYSTEM STRENGHTENING SCHEME-XVIII	PGCIL	02/2009	11/2011	03/2016	509.66	52
115	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER	PGCIL	04/2010	01/2015	03/2016	4404.57	14
116	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A	PGCIL	09/2010	03/2013	10/2015	2074.86	31
117	NORTHERN REGION SYSTEM STRENGHENING SCHEME XVI	PGCIL	07/2010	07/2013	11/2015	752.64	28
118	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A	PGCIL	05/2010	01/2013	09/2015	250.03	32
119	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	12/2016	1272.8	49
120	DHUKWAN SMALL HYDRO PROJECT	THDCIL	05/2011	02/2014	09/2017	195.42	43
121	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	06/2017	5353	37
122	KBUNL-MUZAFFARPUR TPP STAGE-II-SUBSIDIARY (2X195 MW)	NTPC	03/2010	01/2013	03/2016	3984.03	38
123	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	12/2016	09/2017	9750.89	9
124	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	10/2016	368.72	123
125	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	08/2015	421.01	25
126	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B	PGCIL	02/2012	10/2014	09/2015	1927.16	11
127	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION	PGCIL	03/2012	09/2014	06/2016	198.63	21
128	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR	PGCIL	03/2012	03/2014	08/2015	213.78	17

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
	PROVISION)						
129	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	03/2012	06/2015	06/2016	9569.76	12
130	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV	PGCIL	11/2011	11/2014	12/2015	723.63	13
131	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B	PGCIL	02/2012	10/2014	03/2016	3201.44	17
132	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	12/2016	11130.19	40
133	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP)	PGCIL	12/2009	08/2012	03/2016	1216.83	43
134	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	03/2016	2144	39
135	TRANSMISSION SYSTEM OF VINDHUACHAL - IV AND RIHAND -III GEN. PROJ.	PGCIL	03/2010	11/2012	08/2015	4672.99	33
136	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B	PGCIL	12/2010	12/2013	09/2015	2743.19	21
137	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	PGCIL	01/2014	04/2016	11/2016	374.63	7
138	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED	PGCIL	12/2011	02/2014	09/2015	552.44	19
139	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	12/2015	297.33	16
140	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	03/2016	1746.65	19
141	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	11/2016	3642.04	10
142	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	09/2008	03/2016	1779.29	90
143	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	03/2018	8692.97	86
144	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	01/2012	01/2015	03/2016	1422.85	14
145	SOLAPUR STPP	NTPC	03/2012	11/2016	08/2017	9395.18	9
146	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID	PGCIL	09/2012	03/2015	09/2015	1508.74	6
147	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C	PGCIL	03/2013	06/2015	08/2016	514.2	14

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
148	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE	MRTP	04/2012	04/2016	03/2017	714.1	11
149	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	SWR	04/2007	03/2013	09/2015	482	30

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
150	TAMLUK DIGHA,LINE DOUBLING (SER)	SER	03/1984	06/2005	12/2019	293.97	174
151	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	03/2017	325	84
152	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	51
153	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	03/2016	1676.31	84
154	KATAKHAL TO BHAIRABI	NFR	04/1998	12/2012	03/2016	227.9	39
155	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP)	M RTP	03/1996	03/2004	03/2016	495.44	144
156	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2017	1500	110
157	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) ,NEFR	NFR	04/2000	12/2008	03/2018	733	111
158	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	NFR	04/2003	03/2011	03/2019	727.56	96
159	PATNA GANGA BRIDGE (NL) , ECR	ECR	04/2001	10/2007	12/2015	624.47	98
160	NEW LINE FROM DIMAPUR TO ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2020	850	60
161	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	03/2019	5300	60
162	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	ER	04/1999	12/2012	09/2015	207.52	33
163	KATI HAR - JOGBANI (GC) (NEFR)	NFR	09/2001	12/2010	03/2018	492.98	87
164	BANKURA - DAMODAR (GC) (SER)	SER	03/1998	03/2005	12/2019	111.9	177
165	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL) , ECR	ECR	04/2002	03/2009	10/2015	921	79
166	ETAWAH-MAINPURI (NL) ,NCR	NCR	04/1997	12/2008	10/2015	120	82
167	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	12/2015	687.2	69
168	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	03/2016	171.1	48
169	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2018	619.34	47
170	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2018	813.34	48
171	UDHAMPUR-SRINAGAR-BARAMULLA (NL) ,NR	NR	03/1995	11/2002	12/2018	2500	193
172	GONDIA-JABALPUR (GC) , (SECR)	SECR	02/1997	03/1998	12/2019	386.3	261

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
173	RANCHI-LOHARDAGA (GC) ,SER	SER	04/1997	06/2004	12/2015	194.07	138
174	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	M RTP	03/2013	03/2016	06/2018	4874.58	27
175	CONSTRUCTION OF NL FROM KUMARGHAT- AGARTALA	NFR	04/1999	03/2007	03/2016	895	108
176	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION	SER	04/2010	03/2015	12/2016	149.9	21

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
177	FOUR LANING OF ORISSA CHATTISHGARH BORDER	NHAI	02/2013	08/2015	02/2016	1232	6
178	SONAPUR TO GUWAHTI (AS-3)	NHAI	12/2003	03/2008	01/2016	245	94
179	BRAMHPUTRA BRIDGE, NH NO-31	NHAI	12/2003	04/2010	01/2016	217.61	69
180	NALBARI T BIJNI (AS-7)	NHAI	12/2003	04/2008	01/2016	208	93
181	NALBARI TO BIJNI (AS-6)	NHAI	12/2003	06/2008	08/2015	225	86
182	GANGA BRIDGE TO RAMDEVI CROSSING PH. II NH-25, KM. 75-80.06	NHAI	12/2003	09/2008	09/2015	155	84
183	VARANASI-AURANGABAD KM. 786 TO KM. 978.40	NHAI	09/2011	03/2014	04/2017	2848	37
184	4-LANING OF BARHI-HAZARIBAGH	NHAI	02/2012	02/2014	09/2015	398	19
185	BHOPAL-SANCHI	NHAI	10/2011	01/2013	12/2015	209	35
186	NIROLI-ROXY-RAJAMUNDA	NHAI	07/2011	01/2014	12/2016	586	35
187	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER	NHAI	11/2011	05/2014	07/2015	909	14
188	PANIKHOLI-RIMOLI	NHAI	03/2012	09/2014	06/2016	1410	21
189	BEAWAR-PALI-PINDWARA	NHAI	12/2011	06/2014	11/2015	2388	17
190	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM)	NHAI	04/2012	04/2014	07/2015	624	15
191	MAIBANG TO LUMDING (AS-24), KM. 111.000 TO KM. 126.450	NHAI	12/2003	11/2008	12/2015	155.04	85
192	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	NHAI	12/2003	05/2008	10/2015	160	89
193	GUWHATI TO NALBARI (AS-4)	NHAI	12/2003	04/2008	08/2015	175.96	88
194	GUWAHATI TO NALBARI (AS-5)	NHAI	12/2003	04/2008	12/2015	198.16	92

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
195	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	NHAI	02/2009	08/2011	09/2016	1693.75	61
196	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	NHAI	12/2011	06/2014	03/2016	1047	21
197	NAGPUR-WAINGANGA BRIDGE	NHAI	04/2012	10/2014	03/2016	484.19	17

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
198	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT TR	01/2007	12/2010	01/2016	366.39	61

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
199	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B	SAIL	11/2012	06/2015	12/2015	313.05	6
200	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS	RINL	07/2011	07/2015	03/2016	877.73	8
201	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	12/2016	15525	19
202	EXPANSION OF BHILAI STEEL PLANT	SAIL	08/2010	03/2013	03/2016	17265	36
203	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP	SAIL	10/2012	09/2014	07/2015	160.48	10
204	EXPANSION OF BOKARO STEEL PLANT	SAIL	05/2010	12/2011	08/2015	6325	44
205	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC)	NMDC	02/2011	05/2013	08/2015	898.55	27
206	CAPTIVE POWER PLANT - 2	RINL	02/2011	09/2013	07/2015	677	22
207	SMS-1 CONVERTERS REVAMPING	RINL	05/2012	07/2015	03/2017	404.16	20
208	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES	SAIL	12/2011	10/2013	12/2015	187.33	26
209	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA	SAIL	06/2012	12/2014	09/2015	237.09	9
210	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH	SAIL	07/2012	08/2014	11/2015	332.65	15

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
211	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS	BSNL	10/2009	10/2010	09/2015	384	59

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
212	FARIDABAD EXTENSION	DMRCL	09/2011	09/2014	08/2015	2494	11
213	DELHI MRTS PHASE-III	DMRCL	09/2011	03/2016	12/2016	38585	9
214	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL	CPWD	12/2012	12/2014	12/2016	188.87	24
215	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	CPWD	02/2014	09/2015	12/2016	156.57	15
216	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	CPWD	11/2012	11/2014	10/2015	270.83	11
217	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB	CPWD	11/2012	02/2015	08/2015	238.43	6
218	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI	CPWD	05/2009	05/2013	11/2015	261.85	30
219	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI	CPWD	05/2012	12/2014	04/2016	405.01	16
220	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	CPWD	07/2012	08/2014	06/2017	884.3	34
221	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	01/2015	12/2015	23136	11
222	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	08/2016	14600	8

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

ATOMIC ENERGY							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	5677	2185
2	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	13171	17270	4099
COAL							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
3	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	NLC	10/2004	06/2009	2030.78	3583.77	1552.99
4	ADRIYALA SHAFT PROJECT	SCCL	12/2009	03/2013	212.34	1228.39	1016.05
5	TUTICORIN THERMAL POWER PROJECT- 2X500 MW	NLC	05/2008	03/2012	4904.54	6602.74	1698.2
HEAVY INDUSTRY							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
6	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	HIPE	04/2011	09/2011	1718	3827.3	2109.3
PETROCHEMICALS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
7	ASSAM GAS CRACKER PROJECT	BCPL	04/2006	04/2012	5460.61	9833.52	4372.91
PETROLEUM							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
8	DEVELOPMENT OF G1 AND GS-15 (ONGCL)	ONGC	04/2003	04/2006	429.82	3955.21	3525.39
9	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	993	1693	700
10	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	871.35	1200	328.65
11	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	ISPRL	01/2006	10/2011	732	1227	495
12	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG	ISPRL	01/2006	10/2011	672	1178.35	506.35
13	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	309.81	462.79	152.98
14	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	666	838.08	172.08
15	REWARI KANPUR PIPELINE PROJECT	HPCL	02/2012	11/2015	1210.64	1446.34	235.7
16	INTEGRATED REFINERY EXPANSION PROJECT	BPCL	03/2012	05/2016	14225	16504	2279
17	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	2059.63	2665.65	606.02

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
18	PARADIP REFINERY PROJECT	IOCL	02/2009	11/2012	29777	34555	4778
19	MH NORTH REDEVELOPMENT PHASE III	ONGC	06/2014	05/2017	5706.47	5813.25	106.78
20	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT (MOPS)	ONGC	03/2011	05/2013	861.79	1256.72	394.93
21	INTEGRATED DEVELOPMENT OF BASSEIN FIELD	ONGC	12/2012	02/2016	3513.07	4619.94	1106.87
POWER							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
22	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	7818.68	3899.09
23	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	15300	9014.67
24	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	477.69	721.81	244.12
25	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	NHPC	09/2005	09/2009	1061.38	1929.15	867.77
26	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	4375.35	6749.18	2373.83
27	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	421.01	1007.68	586.67
28	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	368.72	1381.71	1012.99
29	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	8692.97	15095.67	6402.7
30	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	09/2008	1779.29	2159.07	379.78
31	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	3642.04	5497.72	1855.68
32	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	1746.65	2228.71	482.06
33	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	573.99	1487.49	913.5
34	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	07/2010	1657	2978.86	1321.86
35	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	2496.9	6476.34	3979.44
36	BARH STPP STAGE -II	NTPC	02/2008	10/2013	7341.04	10852.46	3511.42
37	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	2491.58	3745.08	1253.5
38	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	3846.3	867.82

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
39	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A	PGCIL	09/2010	03/2013	2074.86	2348.37	273.51
40	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C	PGCIL	03/2011	03/2014	2569.25	3105.51	536.26
RAILWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
41	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	NCR	04/1986	03/1994	158.77	608.02	449.25
42	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR (NL) , NEFR	NFR	04/1983	N.A.	36.8	1336.57	1299.77
43	CALICUT-MANGALORE (DL) (SR)	SR	02/1996	N.A.	240	579.37	339.37
44	KARUR-SALEM (NL) , SR	SR	02/1997	N.A.	155.55	800	644.45
45	KATIHAR - JOGBANI (GC) (NEFR)	NFR	09/2001	12/2010	492.98	1727.27	1234.29
46	GULBARGA-BIDAR, SCR (NL)	SCR	02/1998	N.A.	242.42	844	601.58
47	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR (SR) (GC)	SR	03/1998	N.A.	280	1122	842
48	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	N.A.	330	1047	717
49	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT (MTP)	M RTP	03/2000	12/2006	1049.69	3404.92	2355.23
50	GADWAL - RAICHUR (NL) , SCR	SCR	04/1998	02/2011	92.63	270	177.37
51	BANKURA - DAMODAR (GC) (SER)	SER	03/1998	03/2005	111.9	2371.85	2259.95
52	JIND-SONEPAT (NL) , NR	NR	01/2004	03/2012	238.56	740	501.44
53	HARIDASPUR-PARADEEP (NL)	RVNL	04/1996	N.A.	301.64	1185.64	884
54	TUMKUR-CHITRADURGA-DAVENGERE NL	SWR	04/2011	N.A.	913	1801.01	888.01
55	PANVEL PEN DOUBLING	CR	04/2006	N.A.	96.16	260.16	164
56	PEN ROHA DOUBLING	CR	04/2007	N.A.	98.74	203	104.26
57	WARDHA-NANDED MAHARASHTRA	CR	04/2008	N.A.	499.3	2501.05	2001.75
58	KATAKHAL TO BHAIRABI	NFR	04/1998	12/2012	227.9	331.4	103.5
59	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2012	603.04	1421.25	818.21
60	OBULAVARIPALLE-KRISHNAPATNAM (RVNL)	RVNL	07/2006	03/2008	743	1117.11	374.11

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
61	MANOHARABAD-KOTHPALL NEW LINE (SCR)	SCR	04/2006	N.A.	378.56	791.59	413.03
62	TIDIVANAM-NAGARI (NL)	SR	09/2006	N.A.	456	1080	624
63	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	1500	4996.19	3496.19
64	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP)	M RTP	03/1996	03/2004	495.44	1781.98	1286.54
65	AHMEDNAGAR-PARLI VAIJNATH (NL) CR	CR	02/1997	N.A.	514.68	2820	2305.32
66	MM FROM PANSKURA-GHATAL NL	SER	04/2011	01/1999	276.69	426	149.31
67	MM FROM BURAMARA-CHAKULIA	SER	04/2008	01/1999	466.48	800	333.52
68	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI	SR	04/1999	01/1999	460.94	1030	569.06
69	GADAG-WADI NL	SWR	04/2013	N.A.	1117	1922	805
70	HARIDWAR-LAKSAR	NR	04/2012	N.A.	219.83	329.97	110.14
71	RAYADURGA-TUMKUR NL	SWR	04/2007	N.A.	970.34	1743	772.66
72	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	N.A.	601.43	800	198.57
73	MULTI MODAL TRANSPORT SYSTEM (MMTS) PHASE-II HYDERABAD	M RTP	04/2012	03/2016	632.68	816.55	183.87
74	LUMDING-HOJAI PATCH DOUBLING PROJECT	NFR	04/2012	N.A.	246.07	364.06	117.99
75	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	N.A.	312.12	453.1	140.98
76	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI	NFR	04/1999	N.A.	523.17	1653.55	1130.38
77	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	N.A.	165.82	435.58	269.76
78	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	394.28	152.76
79	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	N.A.	242.22	679.57	437.35
80	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	N.A.	4083.02	5307.9	1224.88
81	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	SR	04/2007	N.A.	247	951.24	704.24
82	MADURAI-BODINAYAKKANUR	SR	04/2008	N.A.	164.41	450	285.59
83	ERODE-PALANI	SR	04/2008	N.A.	288.57	603.22	314.65

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
84	NEW COOCHBEHAR TO SAMUKTALA	NFR	04/2011	N.A.	209.77	441.45	231.68
85	DIMAPUR-TIZIT NL	NFR	04/2013	N.A.	4274	4487.7	213.7
86	AGARTALA-AKHAURA NL	NFR	04/2012	N.A.	252	886.65	634.65
87	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	03/2007	895	1242.25	347.25
88	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	NFR	04/2010	N.A.	221.42	563.13	341.71
89	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	SR	04/2008	N.A.	822.39	1280.83	458.44
90	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	SR	04/1998	N.A.	271.24	520	248.76
91	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	SR	04/1999	N.A.	198.68	556.64	357.96
92	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	SR	04/2013	N.A.	839	1500	661
93	CHENNAI-CUDDALORE VIA MAMALLAPURAM	SR	04/2008	N.A.	523.52	1200	676.48
94	HAJIPUR-RAMDAYALUNAGAR DOUBLING	ECR	04/2013	N.A.	213.01	367.17	154.16
95	MOTIHARI-SITAMARHI (NL)	ECR	04/2006	N.A.	211	926.09	715.09
96	SAKRI-HASANPUR ROAD (NL)	ECOR	04/1999	N.A.	175.69	325	149.31
97	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	N.A.	258.2	365	106.8
98	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	12/2015	309.44	583	273.56
99	BHADUTOLA-JHARGRAM VIA LALGARH (NL)	SER	04/2011	N.A.	289.64	760	470.36
100	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	N.A.	553.63	1009	455.37
101	BOWAICHANDI-ARAMBAGH	SER	04/2010	N.A.	267.37	434	166.63
102	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR	NCR	04/2010	02/2019	622.41	2030.5	1408.09
103	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	NWR	04/2010	N.A.	739.65	872.22	132.57
104	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTURGARH-UDAIPUR	NWR	04/2013	N.A.	456	855.16	399.16
105	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	1176.09	3845.6	2669.51
106	RATLAM-DUNGARPUR VIA BANSWARA (NL)	NWR	04/2011	N.A.	2082.75	3500	1417.25

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
107	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	N.A.	446	685.17	239.17
108	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	N.A.	320.66	913.48	592.82
109	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	4190	2850.52
110	KISHANGANJ JALALGARH, NL, NEFR	NFR	04/2008	N.A.	282.92	565.13	282.21
111	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	813.34	2876	2062.66
112	LUMDING-SILCHAR JIRIBAM, BADARPUR- BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	1676.31	5500	3823.69
113	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	5300	7986.04	2686.04
114	NEW LINE FROM DIMAPUR TO ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	850	2973.42	2123.42
115	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	N.A.	300	827.73	527.73
116	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	N.A.	200	496.24	296.24
117	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	NFR	12/2006	03/2011	170	485	315
118	CHHAPRA-BALLIA UP	NER	03/2013	N.A.	295	494.92	199.92
119	BANGLORE - SATYAMANGALAM (NL) (SWR)	SWR	04/1996	N.A.	138	1382.78	1244.78
120	HASSAN-BANGALORE VIA SHRAVANA- BELGOLA (NL), SWR	SWR	02/1997	N.A.	295	1289.92	994.92
121	HUBLI-ANKOLA (NL), SWR	SWR	04/1997	N.A.	227	2135	1908
122	RANCHI-LOHARDAGA (GC), SER	SER	04/1997	06/2004	194.07	335	140.93
123	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	293.97	1428	1134.03
124	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	393.46	1026	632.54
125	GONDIA-JABALPUR (GC), (SECR)	SECR	02/1997	03/1998	386.3	1544.4	1158.1
126	MACHERLA-NALGONDA (NL) (SCR)	SCR	07/1998	07/2008	125	480	355
127	MUNEERABAD-MAHABOONAGAR (NL), SCR	SCR	04/1997	N.A.	218.24	645	426.76
128	ANGAMALI-SABARIMALA (N.L.) (SR)	SR	10/1998	N.A.	550	1566	1016
129	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL (SCR)	SCR	12/1994	N.A.	124.43	925.3	800.87

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
130	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	N.A.	826.57	1143.6	317.03
131	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	N.A.	679.27	1111.99	432.72
132	TIRUCHIRAPPALI-NAGORE-KARAIKKAL (SR) (GC)	SR	09/1995	N.A.	100	980	880
133	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	SWR	04/2007	03/2013	482	874.57	392.57
134	NANDYAL-YERRAGUNTALA (NL) , SCR	SCR	03/1996	02/2009	155.74	883	727.26
135	RAJATGARH-BARANG (LD) , ECR	RVNL	04/1999	02/2009	166.16	288	121.84
136	DALLI-RAJHARA - RAOGHAT (PART OF DALLI-RAJHARA-JAGDALPUR) , NL, RVNL	RVNL	04/1995	12/2012	304	968.6	664.6
137	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	325	1564.54	1239.54
138	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD) , NR	NR	03/2002	06/2007	625.3	847.75	222.45
139	UDHAMPUR-SRINAGAR-BARAMULLA (NL) , NR	NR	03/1995	11/2002	2500	19565	17065
140	NANGALDAM-TALWARA (NL) , NR	NR	03/1981	07/2012	450	2100	1650
141	KANPUR-KASGANJ-MATHURA (GC) , NER	NER	03/1997	N.A.	677.97	1651.54	973.57
142	PATNA GANGA BRIDGE (NL) , ECR	ECR	04/2001	10/2007	624.47	2921	2296.53
143	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	NFR	04/2003	03/2011	727.56	6570.75	5843.19
144	KHURDA ROAD-BOLANGIR (NL) ECR	ECOR	04/1994	N.A.	470.21	1995.25	1525.04
145	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) , NEFR	NFR	04/2000	12/2008	733	2531.34	1798.34
146	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	541	378.13
147	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	12/2009	108	432.72	324.72
148	JAYANAGAR-DARBHANGA-NARKATIA GANJ (GC) , ECR	ECR	04/1997	03/2012	501.69	1043.56	541.87
149	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	1630.97	1383.31
150	SHIMOGA-HARIHAR NL	SWR	04/2011	N.A.	562.74	832.47	269.73
151	SRINIVASA-PURA-MADANAPALLI NL	SWR	04/2013	N.A.	296	466.65	170.65
152	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	SWR	04/2013	N.A.	558	692.43	134.43

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
153	BHANUPALI-BILASPUR BERI NL	NR	04/2008	N.A.	1046.88	2966.99	1920.11
154	ROHTAK-MEHAM HANSI	NR	04/2012	N.A.	287	576.18	289.18
155	AKOLA-KHANDWA GC AKOLA-AKOT	SCR	04/2008	N.A.	184.26	2000	1815.74
156	BAGALKOT-KUDACHI NL	SWR	04/2010	N.A.	377.93	986.3	608.37
157	MUNIRABAD (GINGERA) -RAICHUR NL	SWR	04/2007	N.A.	179.65	1350.91	1171.26
158	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	SR	09/2006	N.A.	125	490	365
159	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	SR	09/2006	N.A.	343.17	914.98	571.81
160	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII' -AGASTIYAMPALLI	SR	09/2007	N.A.	404.19	1383.45	979.26
161	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	687.2	800	112.8
162	RAICHUR-GUNTAKAL (DL) (SCR)	RVNL	04/2003	12/2007	136.62	289.93	153.31
163	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	133.41	276	142.59
164	SUKINDA ROAD - ANGUL (NL) (ECOR)	RVNL	04/1998	02/2015	183.23	818.29	635.06
165	CHHINDWARA - NAGPUR (GC) (SECR)	SECR	04/2005	N.A.	383.79	1101.16	717.37
166	VIRAMGAM-BHILDI (WR) ,GC	WR	04/1990	N.A.	155.66	548.01	392.35
167	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	332.92	477.88	144.96
168	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	619.34	2820.25	2200.91
169	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	171.1	275.08	103.98
170	ETAWAH-MAINPURI (NL) ,NCR	NCR	04/1997	12/2008	120	245.39	125.39
171	MAHARAJGANJ-MASRAKH (NL) - NER	NER	04/2003	N.A.	218.19	343	124.81
172	RAMGANJMUNDI-BHOPAL (NL) ,WCR	WCR	04/2001	N.A.	470.92	1225.9	754.98
173	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL) , ECR	ECR	04/2002	03/2009	921	2363	1442

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

ROAD TRANSPORT AND HIGHWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
174	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	199.81	385.13	185.32
175	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	196	331.23	135.23
176	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	155.04	280.13	125.09
177	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	1108	2288	1180
SHIPPING AND PORTS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
178	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL	MUMBAI PORT	11/2007	12/2010	1228	1460	232
179	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	03/2007	04/2009	245.67	373.22	127.55
180	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT	01/2007	12/2010	366.39	669.46	303.07
STEEL							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
181	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	343	488.4	145.4
182	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	RINL	10/2005	10/2009	8692	12291	3599
URBAN DEVELOPMENT							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
183	BANGALORE METRO RAIL PROJECT	M RTP	05/2006	06/2011	6395	11609	5214

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	10/2015	1,3171.00	1,7270.00	4099	82
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	09/2016	3492.00	5677.00	2185	72

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
3	TUTICORIN THERMAL POWER PROJECT- 2X500 MW	NLC	05/2008	03/2012	08/2015	4904.54	6602.74	1698.2	41
4	ADRIYALA SHAFT PROJECT	SCCL	12/2009	03/2013	03/2016	212.34	1228.39	1016.05	36
5	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	NLC	10/2004	06/2009	07/2015	2030.78	3583.77	1552.99	73

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
6	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	HIPE	04/2011	09/2011	12/2017	1718.00	3827.30	2109.3	75

PETROCHEMICALS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
7	ASSAM GAS CRACKER PROJECT	BCPL	04/2006	04/2012	09/2015	5460.61	9833.52	4372.91	41

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
8	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	06/2016	871.35	1200.00	328.65	15
9	INTEGRATED DEVELOPMENT OF BASSEIN FIELD	ONGC	12/2012	02/2016	12/2017	3513.07	4619.94	1106.87	22
10	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	01/2016	993.00	1693.00	700	48
11	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	ISPRL	01/2006	10/2011	01/2016	732.00	1227.00	495	51
12	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT (MOPS)	ONGC	03/2011	05/2013	12/2015	861.79	1256.72	394.93	31

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)	
13	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	10/2016	309.81	462.79	152.98	24
14	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	05/2016	2059.63	2665.65	606.02	14
15	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	11/2016	666.00	838.08	172.08	12
16	PARADIP REFINERY PROJECT	IOCL	02/2009	11/2012	10/2015	2,9777.00	3,4555.00	4778	35

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
17	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	08/2015	421.01	1007.68	586.67	25
18	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2018	2978.48	3846.30	867.82	69
19	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	03/2017	4375.35	6749.18	2373.83	66
20	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2019	2491.58	3745.08	1253.5	78
21	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	03/2017	2496.90	6476.34	3979.44	87
22	TEHRI PUMPED STORAGE PLANT (1000MW)	THDCIL	07/2006	07/2010	05/2018	1657.00	2978.86	1321.86	94
23	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	10/2016	368.72	1381.71	1012.99	123
24	BARH STPP (3X660MW) NTPC	NTPC	02/2005	01/2011	03/2018	8692.97	1,5095.67	6402.7	86
25	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	11/2016	3642.04	5497.72	1855.68	10
26	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2018	3919.59	7818.68	3899.09	111
27	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	NHPC	09/2005	09/2009	06/2016	1061.38	1929.15	867.77	81
28	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	03/2016	477.69	721.81	244.12	66

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

Sn	Project	DOA	DOC Original	DOC Anticipa ted	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)	
29	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C	PGCIL	03/2011	03/2014	08/2015	2569.25	3105.51	536.26	17
30	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A	PGCIL	09/2010	03/2013	10/2015	2074.86	2348.37	273.51	31
31	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	03/2016	573.99	1487.49	913.5	31
32	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	03/2016	1746.65	2228.71	482.06	19
33	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	09/2008	03/2016	1779.29	2159.07	379.78	90

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
34	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	03/2007	03/2016	895.00	1242.25	347.25	108
35	GONDIA-JABALPUR (GC) , (SECR)	SECR	02/1997	03/1998	12/2019	386.30	1544.40	1158.1	261
36	UDHAMPUR-SRINAGAR-BARAMULLA (NL) ,NR	NR	03/1995	11/2002	12/2018	2500.00	1,9565.00	17065	193
37	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2018	813.34	2876.00	2062.66	48
38	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	03/2019	5300.00	7986.04	2686.04	60
39	KATIHAR - JOGBANI (GC) (NEFR)	NFR	09/2001	12/2010	03/2018	492.98	1727.27	1234.29	87
40	BANKURA - DAMODAR (GC) (SER)	SER	03/1998	03/2005	12/2019	111.90	2371.85	2259.95	177
41	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL) , ECR	ECR	04/2002	03/2009	10/2015	921.00	2363.00	1442	79
42	ETAWAH-MAINPURI (NL) ,NCR	NCR	04/1997	12/2008	10/2015	120.00	245.39	125.39	82
43	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	12/2015	687.20	800.00	112.8	69
44	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	03/2016	171.10	275.08	103.98	48

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

Sn	Project	DOA	DOC Original	DOC Anticipa ted	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)	
45	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2018	619.34	2820.25	2200.91	47
46	KATAKHAL TO BHAIRABI	NFR	04/1998	12/2012	03/2016	227.90	331.40	103.5	39
47	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP)	M RTP	03/1996	03/2004	03/2016	495.44	1781.98	1286.54	144
48	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2017	1500.00	4996.19	3496.19	110
49	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) ,NEFR	NFR	04/2000	12/2008	03/2018	733.00	2531.34	1798.34	111
50	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	NFR	04/2003	03/2011	03/2019	727.56	6570.75	5843.19	96
51	PATNA GANGA BRIDGE (NL) , ECR	ECR	04/2001	10/2007	12/2015	624.47	2921.00	2296.53	98
52	NEW LINE FROM DIMAPUR TO ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2020	850.00	2973.42	2123.42	60
53	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	03/2016	1676.31	5500.00	3823.69	84
54	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	4190.00	2850.52	51
55	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	03/2017	325.00	1564.54	1239.54	84
56	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	12/2019	293.97	1428.00	1134.03	174
57	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	SWR	04/2007	03/2013	09/2015	482.00	874.57	392.57	30
58	RANCHI-LOHARDAGA (GC) , SER	SER	04/1997	06/2004	12/2015	194.07	335.00	140.93	138

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
59	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	12/2015	155.04	280.13	125.09	85

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipa ted	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
60	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT TRU	01/2007	12/2010	01/2016	366.39	669.46	303.07	61

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

List of Projects Ahead of Schedule w.r.t. Latest Schedule

(July 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>POWER</u>						
1	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154]	10/2013	1,315.90 -	1,315.90	508.77	10/2016 -	12/2015
	Total		1,315.90 -	1,315.90	508.77		
	<u>COAL</u>						
2	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	3.52	03/2021 -	03/2017
	Total		555.52 -	555.52	3.52		
	<u>PETROLEUM</u>						
3	MARKETING TOP AT KORBA - [N16000186]	1/2011	141.86 -	232.00	147.60	09/2016 -	12/2015
4	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]	7/2014	419.04 -	419.04	153.06	01/2017 -	06/2016
	Total		560.90 -	651.04	300.66		
	<u>POWER</u>						
5	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]	3/2015	1,071.24	1,071.24	-	10/2017 -	09/2017
	Total		1,071.24 -	1,071.24	.00		
	<u>PETROLEUM</u>						
6	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]	11/2014	6,068.80 -	6,068.80	401.81	04/2019 -	03/2019
	Total		6,068.80 -	6,068.80	401.81		
	<u>POWER</u>						
7	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I) - [N18000198]	5/2015	312.94	312.94	-	06/2016 -	05/2016
	Total		312.94 -	312.94	.00		
	Grand Total		9,885.30	9,975.44	1,214.76		

List of Projects on schedule w.r.t. Latest Schedule

(July 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [N06000122]	9/2003	3,492.00 -	5,677.00	5,031.21	09/2010 09/2016	09/2016
	Total		3,492.00 -	5,677.00	5,031.21		
	<u>COAL</u>						
2	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
3	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	5/2015	397.09 -	397.09	-	03/2019 -	03/2019
4	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]	5/2014	479.15 -	479.15	-	03/2019 -	03/2019
5	GOKUL - [N06000120]	11/2014	267.67 -	267.67	152.29	03/2018 -	03/2018
6	AMERA OC RCE - [N06000123]	2/2015	335.97 -	335.97	29.73	03/2018 -	03/2018
7	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	11.77	03/2021 -	03/2021
8	BHANEAGAON OC - [N06000121]	2/2015	187.94 -	187.94	40.78	03/2023 -	03/2023
9	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	92.65	03/2018 -	03/2018
10	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	114.82	03/2020 -	03/2020
11	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]	4/2012	258.56 -	258.56	84.31	03/2016 -	03/2016
12	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	486.27	71.01	03/2016 -	03/2016
13	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	764.69	03/2023 03/2023	03/2023
14	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	5.43	03/2023 03/2023	03/2023
15	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]	5/2014	337.66 -	337.66	-	03/2019 -	03/2019
16	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	26.37	03/2021 -	03/2021
17	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	0.56	03/2026 -	03/2026
18	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	76.43	03/2020 -	03/2020

(July 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
19	DINESH OCP - [N06000118	11/2014	611.16 -	611.16	6.08	03/2020 -	03/2020
20	KAPURIA UG(PSLW) - [N06000108	8/2011	988.35 -	988.35	45.15	04/2017 04/2017	04/2017
21	MAKARDHOKRA I OC - [N06000119	9/2014	266.23 -	266.23	81.08	03/2021 -	03/2021
22	MOONIDIH XV SEAM UG - [N06000098	8/2011	1,230.27 -	1,230.27	42.39	04/2015 04/2019	04/2019
23	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109	8/2012	1,055.05 -	1,055.05	156.87	03/2018 -	03/2018
24	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095	6/2011	5,907.11 -	5,907.11	1,008.61	12/2015 04/2018	04/2018
25	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082	11/2009	150.59 -	198.59	111.96	03/2016 -	03/2016
26	KULDA EXPN OC. (5.00 MTY) - [N06000115	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
27	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010	12/2009	1,352.04 -	1,143.54	804.28	03/2016 -	03/2016
28	NEW MAJRI UG TO OC - [N06000128	5/2015	295.56 -	295.56	59.83	03/2019 -	03/2019
29	CHHAL OC SEAM -III (6.00 MTY) - [N06000104	12/2013	610.63 -	610.33	-	03/2022 -	03/2022
30	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124	12/2014	357.80 -	357.80	108.44	03/2021 -	03/2021
31	AMRAPALI OC(12MTY) - [N06000103	2/2012	858.11 -	858.11	107.24	03/2020 -	03/2020
32	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034	12/2007	490.10 -	490.10	203.68	03/2017 -	03/2017
33	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087	12/2009	510.85 -	510.85	223.15	03/2016 -	03/2016
	Total		34,626.26 -	34,521.28	4,429.60		
	<u>FERTILISERS</u>						
34	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009	10/2014	197.79 -	197.79	24.66	11/2016 -	11/2016
	Total		197.79 -	197.79	24.66		
	<u>MINES</u>						
35	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007	9/2011	1,856.00 -	1,856.00	-	09/2017 -	09/2017
	Total		1,856.00 -	1,856.00	.00		
	<u>PETROLEUM</u>						

(July 2015)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
36	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	1,217.33	03/2015 05/2016	05/2016
37	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]	10/2013	429.06 -	429.06	357.59	10/2014 10/2015	10/2015
38	DAMAN DEVELOPMENT PROJECT - [N16000198]	8/2014	6,086.08 -	6,086.08	84.54	05/2019 03/2020	03/2020
39	TWENTY NOS. FEEDER GAS LINES - [N16000192]	3/2009	228.64 -	214.19	130.94	12/2016 -	12/2016
40	IOR OF B-173A FIELD - [N16000140]	1/2012	352.49 -	352.49	128.12	03/2014 05/2016	05/2016
41	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]	3/2014	2,476.82 -	2,476.82	149.73	12/2018 -	12/2018
42	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	6/2014	5,706.47 -	5,813.25	1,553.25	05/2017 05/2017	05/2017
43	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]	6/2010	2,523.00 -	2,523.00	1,528.40	01/2014 12/2015	12/2015
44	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]	3/2012	2,592.17 -	2,592.17	541.46	05/2014 05/2016	05/2016
45	PARADIP LPG IMPORT FACILITY - [N16000196]	1/2015	690.00 -	690.00	-	07/2018 -	07/2018
46	RESID UPGRADATION PROJECT - [N16000184]	2/2011	3,110.36 -	3,110.36	799.71	11/2015 07/2016	07/2016
47	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	7/2011	352.56 -	450.55	10.60	03/2017 -	03/2017
48	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]	3/2014	238.50 -	238.50	1.07	03/2017 -	03/2017
49	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00 -	3,150.00	108.21	09/2017 -	09/2017
50	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	2/2012	666.00 -	838.08	481.49	11/2015 11/2016	11/2016
51	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]	6/2007	736.65 -	736.65	481.63	09/2011 12/2015	12/2015
52	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]	12/2011	160.00 -	160.00	2.47	02/2016 02/2016	02/2016
53	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]	5/2015	257.87 -	257.87	5.37	11/2016 -	11/2016
54	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]	9/2011	202.25 -	160.16	60.63	07/2016 -	07/2016
55	MEHESANA REDEVELOPMENT PROJECT - [N16000121]	11/2010	3,823.00 -	3,823.00	1,076.57	04/2015 12/2017	12/2017
56	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]	4/2010	270.00 -	215.66	-	06/2012 11/2015	11/2015
57	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]	12/2012	3,513.07 -	4,619.94	336.33	02/2016 12/2017	12/2017
58	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79	237.49	10/2014 10/2016	10/2016

(July 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
59	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]	1/2010	723.64 -	723.64	-	03/2013 06/2016	06/2016
60	CRU TO ISOMERIZATION (ISOM) - [N16000200]	10/2011	725.00 -	725.00	23.91	11/2016 -	11/2016
61	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]	4/2013	284.82 -	284.82	-	04/2015 05/2017	05/2017
62	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]	2/2014	163.88 -	163.88	25.70	07/2016 -	07/2016
63	CONSTRUCTION OF 6 ETPS - [N16000117]	3/2009	317.64 -	240.95	117.49	09/2012 12/2015	12/2015
64	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	3/2012	14,225.00 -	16,504.00	7,147.44	05/2016 -	05/2016
65	REWARI KANPUR PIPELINE PROJECT - [N16000145]	2/2012	1,210.64 -	1,446.34	1,066.43	11/2015 -	11/2015
	Total		57,585.05 -	62,154.90	17,673.90		
	<u>POWER</u>						
66	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	141.00	08/2017 -	08/2017
67	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	12,532.44	1,713.00	08/2018 -	08/2018
68	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	1/2015	203.28 -	203.28	0.20	07/2017 -	07/2017
69	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	1/2013	12,964.60 -	12,964.60	3,767.88	01/2018 -	01/2018
70	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]	3/2015	197.40 -	197.40	-	04/2018 -	04/2018
71	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	488.30	03/2018 -	03/2018
72	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 -	522.29	30.00	11/2016 -	11/2016
73	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]	9/2013	1,575.30 -	1,575.30	370.20	05/2016 -	05/2016
74	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,476.34	3,964.79	12/2009 03/2017	03/2017
75	WARDHA-HYDERABAD 765 KV LINK - [N18000183]	1/2015	3,662.02 -	3,662.02	62.90	05/2018 -	05/2018
76	VINDHYACHAL STPP STAGE-V - [N18000134]	5/2012	3,180.40 -	3,180.40	1,981.00	08/2015 -	08/2015
77	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]	6/2014	400.47 -	400.47	10.40	04/2017 -	04/2017
78	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]	8/2014	188.75 -	188.75	1.00	02/2017 -	02/2017

(July 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
79	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,364.52	278.34	04/2016 -	04/2016
80	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	11,846.00	4,529.00	06/2017 -	06/2017
81	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]	4/2015	1,479.30 -	1,479.30	31.40	04/2017 -	04/2017
82	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]	3/2015	1,394.52 -	1,394.52	-	05/2017 -	05/2017
83	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B [N18000165]	3/2014	155.57 -	155.57	1.00	05/2016 -	05/2016
84	KUDGI STPP STAGE 1 - [N18000131]	1/2012	15,166.19 -	15,166.19	8,655.00	01/2017 -	01/2017
85	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID [N18000169]	8/2014	288.49 -	288.49	23.40	02/2017 -	02/2017
86	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV [N18000152]	9/2013	680.69 -	680.69	298.89	03/2016 -	03/2016
87	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58 -	14,366.58	2,140.00	02/2019 -	02/2019
88	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]	5/2014	829.98 -	829.98	2.00	08/2016 -	08/2016
89	MOUDA STPP STAGE 2 - [N18000132]	3/2012	7,921.47 -	7,921.47	4,309.00	09/2016 -	09/2016
90	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) [N18000179]	12/2014	6,517.36 -	6,517.36	111.80	04/2018 -	04/2018
91	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]	4/2015	3,705.61 -	3,705.61	57.40	04/2018 -	04/2018
92	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII [N18000159]	2/2014	908.08 -	908.08	53.70	06/2016 -	06/2016
93	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	2/2014	196.58 -	196.58	1.00	02/2016 -	02/2016
94	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION [N18000186]	3/2015	550.06 -	550.06	1.60	03/2018 -	03/2018
95	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	717.00	03/2019 -	03/2019
96	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]	2/2014	378.71 -	378.71	81.90	10/2016 -	10/2016
97	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP [N18000180]	1/2015	268.80 -	268.80	0.80	03/2018 -	03/2018
98	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	11,638.55	3,675.00	09/2017 -	09/2017

(July 2015)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
99	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.84	119.00	09/2019 -	09/2019
100	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]	5/2014	303.07 -	303.07	2.30	07/2016 -	07/2016
101	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX [N18000158]	2/2014	539.82 -	539.82	62.50	06/2016 -	06/2016
102	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) [N18000181]	1/2015	871.62 -	871.62	1.90	11/2017 -	11/2017
103	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]	10/2014	8,112.12 -	8,112.12	-	04/2020 -	04/2020
104	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]	11/2014	972.42 -	972.42	-	11/2017 -	11/2017
105	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]	2/2014	243.53 -	243.53	146.50	08/2016 -	08/2016
106	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]	2/2014	167.40 -	167.40	68.80	12/2015 -	12/2015
107	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]	5/2015	780.33 -	780.33	-	07/2017 -	07/2017
108	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]	7/2013	3,363.12 -	3,363.12	698.00	12/2016 -	12/2016
	Total		150,183.53 -	154,162.97	38,597.90		
	<u>RAILWAYS</u>						
109	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]	4/2010	622.41 -	2,030.50	3.61	02/2019 -	02/2019
110	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	4/2011	299.60 -	299.60	1.10	03/2017 -	03/2017
111	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	4/2012	632.68 -	816.55	-	03/2016 -	03/2016
112	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	4/2008	5,300.00 -	7,986.04	2,443.62	03/2014 03/2019	03/2019
113	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	1,176.09 -	3,845.60	2.33	02/2020 -	02/2020
114	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	4/2010	2,913.51 -	2,619.02	-	03/2016 -	03/2016
115	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	4/2012	148.77 -	209.00	2.64	12/2016 -	12/2016
116	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	4/2006	325.00 -	1,564.54	420.71	03/2010 03/2017	03/2017
117	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	4/2010	3,951.98 -	3,951.98	-	03/2016 -	03/2016

						(July 2015)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
118	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	4/2010	423.66 -	423.66	163.59	03/2017 -	03/2017
119	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	4/2006	850.00 -	2,973.42	10.44	03/2015 03/2020	03/2020
	Total		16,643.70 -	26,719.91	3,048.04		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
120	2-LANING WITH PS OF JHALAWAR-RAJASTHAN-MP. BORDER - [N24000237]	1/2014	177.32 -	177.32	86.65	01/2016 -	01/2016
121	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239]	1/2014	368.15 -	368.15	27.32	01/2016 -	01/2016
122	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 -	208.00	-	04/2008 01/2016	01/2016
123	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	-	09/2015 -	09/2015
124	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236]	10/2013	677.79 -	677.79	59.09	04/2016 -	04/2016
125	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]	10/2013	283.25 -	283.25	-	10/2015 -	10/2015
126	NALBARI TO BIJNI (AS-6) - [N24000047]	12/2003	225.00 -	225.00	-	06/2008 08/2015	08/2015
127	GUWAHATI TO NALBARI (AS-5) - [N24000046]	12/2003	198.16 -	198.16	242.40	04/2008 12/2015	12/2015
128	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]	11/2013	1,916.79 -	1,916.79	-	11/2016 -	11/2016
129	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	163.30	12/2015 -	12/2015
130	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	-	04/2010 01/2016	01/2016
131	GUWAHATI TO NALBARI (AS-4) - [N24000038]	12/2003	175.96 -	175.96	-	04/2008 08/2015	08/2015
132	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]	3/2014	240.10 -	240.10	-	03/2016 -	03/2016
133	SONAPUR TO GUWAHATI (AS-3) - [N24000044]	12/2003	245.00 -	245.00	-	03/2008 01/2016	01/2016
134	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR - [N24000238]	1/2014	158.04 -	158.04	2.67	12/2015 -	12/2015
135	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]	12/2003	160.00 -	160.00	-	05/2008 10/2015	10/2015
136	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]	7/2010	1,987.00 -	1,987.00	-	07/2015 -	07/2015
137	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	4/2014	1,266.60 -	1,266.60	-	09/2016 -	09/2016

(July 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
138	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228	6/2013	1,287.95 -	1,287.95	-	11/2015 -	11/2015
	Total		13,490.96 -	13,582.91	581.43		
	<u>STEEL</u>						
139	REBUILDING OF COB-7 AT BSL - [N12000083	10/2013	245.67 -	245.67	51.94	05/2016 -	05/2016
140	TURBO BLOWER - 5 - [N12000092	12/2009	280.00 -	280.00	13.77	09/2016 -	09/2016
141	NMDC INTEGRATED STEEL PLANT - [N12000086	1/2010	15,525.00 -	15,525.00	7,580.18	05/2015 12/2016	12/2016
142	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094	4/2015	3,127.30 -	3,127.30	5.18	04/2018 -	04/2018
143	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096	5/2015	1,154.18 -	1,154.18	-	12/2017 -	12/2017
144	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084	6/2014	708.91 -	708.91	159.27	04/2016 -	04/2016
145	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	25.49	10/2016 -	10/2016
146	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095	3/2015	1,034.01 -	1,034.01	-	10/2017 -	10/2017
147	ALTERNATE GAS NETWORK AT BSL - [N12000093	3/2015	255.19 -	255.19	-	03/2018 -	03/2018
148	3RD CONVERTER AND 4TH CASTER - [N12000088	7/2011	974.76 -	974.76	147.85	07/2016 -	07/2016
	Total		23,648.02 -	23,793.42	7,983.68		
	<u>TELECOMMUNICATIONS</u>						
149	NETWORK FOR SPECTRUM - [N26000101	3/2012	13,334.00 -	13,334.00	-	07/2015 -	07/2015
	Total		13,334.00 -	13,334.00	.00		
	<u>URBAN DEVELOPMENT</u>						
150	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058	2/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019
151	NAGPUR METRO RAIL - [N28000085	8/2014	8,680.00 -	8,680.00	-	03/2018 -	03/2018
152	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 -	1,219.21	-	07/2017 -	07/2017
153	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080	6/2012	4,264.00 -	4,264.00	557.63	11/2019 -	11/2019

(July 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
154	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076	6/2014	157.84 -	157.84	-	03/2017 -	03/2017
155	KOCHI METRO RAIL PROJECT - [N28000081	7/2012	5,181.79 -	5,181.79	-	07/2017 -	07/2017
156	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060	4/2014	332.72 -	332.72	-	09/2016 -	09/2016
	Total		46,240.70 -	46,240.70	557.63		
	Grand Total		361,298.01	382,240.88	77,928.05		

List of ongoing projects having cost overrun w.r.t. to revised schedule

(July 2015)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost (Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
1	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]	10/2012	217.60 -	244.10	03/2015 -	09/2015	12.18
	Total		217.60 -	244.10			
	<u>COAL</u>						
2	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	03/2016 -	03/2016	31.87
3	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	479.63	03/2013 -	03/2017	0.02
	Total		630.12 -	678.22			
	<u>HEAVY INDUSTRY</u>						
4	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78
	Total		1,718.00 -	3,827.30			
	<u>PETROCHEMICALS</u>						
5	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	9,833.52	04/2012 -	09/2015	80.08
	Total		5,460.61 -	9,833.52			
	<u>PETROLEUM</u>						
6	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	450.55	03/2017 -	03/2017	27.79
7	MARKETING TERMINAL AT PARADEEP - [N16000168]	07/2009	199.75 -	239.73	07/2013 -	10/2015	20.02
8	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]	10/2013	429.06 -	429.06	10/2014 -	10/2015	0.00
9	MARKETING TOP AT KORBA - [N16000186]	01/2011	141.86 -	232.00	09/2016 -	12/2015	63.54
10	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	03/2012	14,225.00 -	16,504.00	05/2016 -	05/2016	16.02

(July 2015)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost (Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
11	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	06/2016	37.72
	Total		16,219.58 -	19,055.34			
	<u>POWER</u>						
12	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	7,818.68	09/2009 -	12/2018	99.48
13	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	15,300.00	09/2010 -	-	143.42
14	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]	09/2005	1,061.38 -	1,929.15	09/2009 -	06/2016	81.76
15	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,745.08	06/2013 -	12/2019	50.31
16	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,497.72	01/2016 -	11/2016	50.95
	Total		17,399.92 -	34,290.63			
	<u>RAILWAYS</u>						
17	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	36.80 274.41	1,336.57	- -	03/2019	3,531.98
18	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37	- -	02/2012	141.40
19	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 -	800.00	- -	-	414.30
20	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	492.98 -	1,727.27	12/2010 -	03/2018	250.37
21	GULBARGA-BIDAR,SCR(NL) - [220100254]	02/1998	242.42 369.70	844.00	- 05/2009	03/2015	248.16
22	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) [220100263]	03/1998	280.00 -	1,122.00	- -	-	300.71
23	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 -	1,047.00	- -	-	217.27
24	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
25	GADWAL - RAICHUR (NL), SCR - [220100270]	04/1998	92.63 -	270.00	02/2011 -	-	191.48
26	BANKURA - DAMODAR (GC) (SER) - [220100277]	03/1998	111.90 -	2,371.85	03/2005 12/2008	12/2019	2,019.62
27	JIND-SONEPAT (NL),NR - [220100280]	01/2004	238.56 -	740.00	03/2012 -	12/2012	210.19
28	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06

(July 2015)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost (Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
29	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]	04/2002	921.00 -	2,363.00	03/2009 -	10/2015	156.57
30	RAMGANJ-MUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	470.92 727.13	1,225.90	- -	03/2017	160.32
31	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	04/2003	218.19 -	343.00	- -	-	57.20
32	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	1,101.16	- -	03/2017	186.92
33	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23 -	818.29	02/2015 -	-	346.59
34	CUTTACK - BARANG (LD) - [220100326]	04/1995	127.13 -	225.00	- -	10/2014	76.98
35	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	276.00	03/2009 03/2009	08/2014	106.88
36	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	810.80	- -	-	0.00
37	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]	04/2003	136.62 -	289.93	12/2007 03/2010	-	112.22
38	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1997	261.70 -	280.00	02/2006 -	-	6.99
39	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41
40	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI [N22000079]	09/2007	404.19 -	1,383.45	- -	-	242.28
41	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	914.98	- -	03/2016	166.63
42	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 -	490.00	- -	-	292.00
43	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	1,080.00	- -	-	136.84
44	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	03/2016	60.77
45	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,820.25	04/2014 -	03/2018	355.36
46	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	332.92 283.95	477.88	03/2012 -	-	43.54
47	VIRAMGAM-BHILDI(WR),GC - [220100062]	04/1990	155.66 -	548.01	- 03/2010	-	252.06
48	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56 -	791.59	- -	-	109.11
49	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 -	1,117.11	03/2008 06/2008	-	50.35
50	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	653.55	03/2014 -	-	0.06
51	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012 -	-	135.68

(July 2015)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost (Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
52	KATAKHAL TO BHAIRABI - [N22000126	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41
53	WARDHA-NANDED MAHARASHTRA - [N22000231	04/2008	499.30 -	2,501.05	- -	-	400.91
54	KALYAN-KASARA 3RD LINE - [N22000233	04/2011	277.70 -	279.70	- -	-	0.72
55	PEN ROHA DOUBLING - [N22000254	04/2007	98.74 -	203.00	- -	03/2015	105.59
56	PANVEL PEN DOUBLING - [N22000255	04/2006	96.16 -	260.16	- -	01/2015	170.55
57	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256	04/2011	913.00 -	1,801.01	- -	-	97.26
58	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257	04/2007	179.65 -	1,350.91	- -	-	651.97
59	BAGALKOT-KUDACHI NL - [N22000258	04/2010	377.93 -	986.30	- -	-	160.97
60	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263	04/2008	184.26 -	2,000.00	- -	-	985.42
61	ROHTAK-MEHAM HANSI - [N22000272	04/2012	287.00 -	576.18	- -	-	100.76
62	BHANUPALI-BILASPUR BERI NL - [N22000273	04/2008	1,046.88 -	2,966.99	- -	-	183.41
63	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276	04/2013	558.00 -	692.43	- -	-	24.09
64	SRINIVASA-PURA-MADANAPALLI NL - [N22000277	04/2013	296.00 -	466.65	- -	-	57.65
65	SHIMOGA-HARIHAR NL - [N22000278	04/2011	562.74 -	832.47	- -	-	47.93
66	RAYADURGA-TUMKUR NL - [N22000279	04/2007	970.34 -	1,743.00	- -	-	79.63
67	WHITE FIELD-KOLAR NL - [N22000280	04/2011	341.05 -	348.85	- -	-	2.29
68	BHADRACHALAM ROAD-SATTUPALLI - [N22000287	04/2010	337.49 -	337.50	- -	-	0.00
69	HARIDWAR-LAKSAR - [N22000289	04/2012	219.83 -	329.97	- -	-	50.10
70	TORANAGALLU-RANJITPURA DL - [N22000298	04/2011	146.75 -	167.50	- -	-	14.14
71	GADAG-WADI NL - [N22000299	04/2013	1,117.00 -	1,922.00	- -	-	72.07
72	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300	04/2013	327.25 -	367.77	- -	-	12.38
73	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303	04/1999	460.94 -	1,030.00	01/1999 -	-	123.46
74	MM FROM BURAMARA-CHAKULIA - [N22000305	04/2008	466.48 -	800.00	01/1999 -	-	71.50
75	MM FROM PANSKURA-GHATAL NL - [N22000309	04/2011	276.69 -	426.00	01/1999 -	-	53.96

(July 2015)

(July 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost (Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
76	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181	02/1997	514.68 -	2,820.00	-	-	447.91
77	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	1,781.98	03/2004 -	03/2016	259.68
78	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	06/2017	233.08
79	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	247.66 -	1,630.97	05/2008 -	-	558.55
80	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240	04/1997	501.69 335.77	1,043.56	03/2012 -	-	108.01
81	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	12/2009 -	06/2015	300.67
82	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257	04/1997	162.87 -	541.00	- -	-	232.17
83	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266	04/2000	733.00 -	2,531.34	12/2008 -	03/2018	245.34
84	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	470.21 -	1,995.25	- -	-	324.33
85	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	6,570.75	03/2011 -	03/2019	803.12
86	KOSI BRIDGE (NL), ECR - [220100304	04/2002	322.95 -	341.41	03/2012 -	-	5.72
87	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76
88	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082	12/2006	170.00 -	485.00	03/2011 -	-	185.29
89	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086	09/2006	200.00 -	496.24	- -	03/2017	148.12
90	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087	09/2006	300.00 -	827.73	- -	03/2019	175.91
91	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124	04/2006	850.00 -	2,973.42	03/2015 -	03/2020	249.81
92	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
93	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127	04/1996	1,676.31 -	5,500.00	03/2009 -	03/2016	228.10
94	AGARTALA SABROOM, NL, NEFR - [N22000099	04/2008	813.34 -	2,876.00	03/2014 -	03/2018	253.60
95	KISHANGANJ JALALGARH, NL, NEFR - [N22000101	04/2008	282.92 -	565.13	- -	03/2018	99.75
96	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	4,190.00	12/2015 -	03/2020	212.81
97	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197	03/1997	677.97 1,062.36	1,651.54	- -	03/2018	143.60

(July 2015)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost (Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
98	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
99	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60
100	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	625.30 408.76	847.75	06/2007 -	-	35.57
101	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	04/2006	325.00 -	1,564.54	03/2010 -	03/2017	381.40
102	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	968.60	12/2012 -	-	218.62
103	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	288.00	02/2009 02/2009	08/2014	73.33
104	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075	09/2006	324.90 -	385.54	03/2010 -	-	18.66
105	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192	03/1996	155.74 164.36	883.00	02/2009 -	03/2015	466.97
106	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	645.00	- -	03/2015	195.55
107	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
108	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,544.40	03/1998 -	12/2019	299.79
109	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	03/2015	160.76
110	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097	03/1984	293.97 -	1,428.00	06/2005 -	12/2019	385.76
111	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	335.00	06/2004 -	12/2015	72.62
112	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	- -	-	840.53
113	HASSAN-BANGALORE VIA SHRAVANA- BELGOLA(NL),SWR [220100183	02/1997	295.00 -	1,289.92	- -	-	337.26
114	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	04/1996	138.00 -	1,382.78	- -	-	902.01
115	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107	04/2007	482.00 -	874.57	03/2013 -	09/2015	81.45
116	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	980.00	- -	-	880.00
117	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123	04/2008	318.24 -	321.62	03/2012 -	-	1.06
118	SAMBALPUR-TALCHER DOUBLING - [N22000315	03/2011	679.27 -	1,111.99	- -	-	63.70
119	JHARSUGUDA-RENGALI DOUBLING - [N22000317	03/2006	201.00 -	230.00	- -	-	14.43
120	KIRANDUL - JAGDALPUR DOUBLING - [N22000318	12/2012	826.57 -	1,143.60	- -	03/2018	38.35

(July 2015)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost (Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
121	DELANG-PURI DOUBLING - [N22000320]	03/2011	165.16 -	234.71	03/2015 -	03/2015	42.11
122	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10
123	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	209.00	12/2016 -	12/2016	40.49
124	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43 -	925.30	- -	02/2014	643.63
125	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	663.01 175.30	725.00	06/1999 -	07/2012	9.35
126	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00 -	1,566.00	- -	-	184.73
127	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	494.92	- -	-	67.77
128	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	685.17	- -	-	53.63
129	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	3,500.00	- -	-	68.05
130	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	262.00	- -	-	10.58
131	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]	04/2013	456.00 -	855.16	- -	-	87.54
132	RATANGARH-SARDARSAHAR (MM OF SADULPUR- BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	-	17.92
133	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	218.39	- -	-	2.34
134	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00	- -	-	62.32
135	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00	- -	12/2019	82.25
136	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
137	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44
138	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	03/2016	88.40
139	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	12/2017	41.36
140	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
141	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
142	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	- -	-	338.91
143	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37

(July 2015)

(July 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost (Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
144	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00 -	1,887.90	- -	03/2019	5.00
145	ATTIPPATTU-PUTTUR - [N22000184]	04/2008	446.87 -	528.00	- -	-	18.16
146	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,200.00	- -	-	129.22
147	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
148	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17
149	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC [N22000188]	04/1998	271.24 -	520.00	- -	-	91.71
150	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,280.83	- -	-	55.74
151	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
152	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	563.13	- -	03/2019	154.33
153	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,242.25	03/2007 -	03/2016	38.80
154	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00 -	886.65	- -	03/2018	251.85
155	DIMAPUR-TIZIT NL - [N22000196]	04/2013	4,274.00 -	4,487.70	- -	03/2020	5.00
156	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77 -	441.45	- -	03/2018	110.44
157	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	288.81	- -	03/2018	1.86
158	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22	- -	-	109.04
159	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	-	173.71
160	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	247.00 -	951.24	- -	03/2015	285.12
161	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	222.95	- -	-	16.29
162	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02 -	5,307.90	- -	03/2020	30.00
163	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	679.57	- -	03/2018	180.56
164	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	03/2017	63.25
165	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	435.58	- -	03/2018	162.68

(July 2015)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost (Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
166	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209	04/1999	523.17 -	1,653.55	- -	03/2018	216.06
167	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210	04/2011	312.12 -	453.10	- -	03/2018	45.17
168	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211	04/2012	246.07 -	364.06	- -	03/2019	47.95
169	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213	04/2012	632.68 -	816.55	03/2016 -	03/2016	29.06
170	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215	04/2011	601.43 -	800.00	- -	-	33.02
	Total		79,170.45 -	200,328.20			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
171	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 -	361.00	02/2009 -	-	28.93
172	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	04/2009 -	-	92.75
173	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	11/2008 -	12/2015	80.68
174	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	331.23	07/2009 -	-	68.99
175	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	-	106.50
176	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221	12/2003	155.00 -	201.66	09/2008 -	09/2015	30.10
177	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	02/2010 -	-	2.29
	Total		2,368.85 -	4,128.46			
	<u>SHIPPING AND PORTS</u>						
178	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016	11/2007	1,228.00 -	1,460.00	12/2010 -	-	18.89
179	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059	03/2007	245.67 -	373.22	04/2009 -	-	51.92
	Total		1,473.67 -	1,833.22			
	<u>STEEL</u>						
180	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	10/2016	42.39
	Total		343.00 -	488.40			

(July 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost (Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	URBAN DEVELOPMENT						
181	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00 -	11,609.00	06/2011 -	-	81.53
	Total		6,395.00 -	11,609.00			
	Grand Total		131,396.80	286,316.39			

List of Delayed Projects w.r.t. Latest Schedule

(July 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL, TAMIL NADU	12/2001	13,171.00 17,270.00	17,270.00	20,713.00	12/2008 -	10/2015	82	-
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 -	11,459.00	6,853.00	12/2015 -	10/2017	22	-
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 -	12,320.00	4,669.00	12/2016 -	05/2018	17	-
	Total		36,950.00 -	41,049.00	32,235.00				
	<u>CIVIL AVIATION</u>								
4	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT (MOHALI) PH - II - [N04000070]AAI, CHANDIGARH	02/2011	452.00 489.00	489.00	468.24	03/2015 -	07/2015	4	-
5	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI, MULTI STATE	10/2012	217.60 -	244.10	0.04	03/2015 -	09/2015	6	-
6	CONSTRUCTION OF NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT - [N04000050]AAI, SIKKIM	01/2009	309.46 -	309.46	357.35	01/2011 06/2016	09/2017	80	15
	Total		979.06 -	1,042.56	825.63				
	<u>COAL</u>								
7	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC, TAMIL NADU	10/2004	2,030.78 3,583.77	3,583.77	3,213.77	06/2009 03/2013	07/2015	73	28
8	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC, TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	6,355.68	03/2012 05/2014	08/2015	41	15
9	WIND POWER PROJECT, KAZHUNEERKULAM, TAMIL NADU - [N06000110]NLC, TAMIL NADU	04/2012	364.75 -	364.75	159.12	10/2014 -	08/2015	10	-
10	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL, ODISHA	01/2005	302.96 -	302.96	146.90	03/2010 -	03/2016	72	-
11	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL, CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,863.12	03/2014 -	03/2016	24	-
12	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL, CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,664.33	03/2014 -	03/2016	24	-
13	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL, UTTAR PRADESH	06/2011	789.88 741.62	741.62	480.93	03/2013 -	03/2016	36	-
14	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL, MADHYA PRADESH	06/2011	746.04 535.10	535.10	382.96	03/2015 -	03/2016	12	-
15	MAGADH OC 20 MTY (CCL) - [N06000015]CCL, JHARKHAND	08/2008	706.40 -	706.40	77.19	07/2012 -	03/2016	44	-
16	ADRIYALA SHAFT PROJECT - [N06000016]SCCL, TELANGANA	12/2009	212.34 1,228.39	1,228.39	859.79	03/2013 09/2012	03/2016	36	42
17	CHURCHA ROUG (1.35MTY) - [N06000046]SECL, CHHATISGARH	06/2008	462.35 -	462.35	298.70	03/2014 -	03/2016	24	-

(July 2015)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
18	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82	153.82	59.12	03/2014	03/2016	24	-
19	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97	418.97	365.16	03/2012	03/2016	48	-
20	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78	209.78	74.10	03/2015	03/2016	12	-
21	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19	181.19	36.60	03/2012	03/2016	48	-
22	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50	321.50	207.27	03/2014	03/2016	24	-
23	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51	163.51	35.92	03/2011	03/2016	60	-
24	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98	210.98	147.70	03/2013	03/2016	36	-
25	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68	264.68	144.13	03/2012	03/2016	48	-
26	MURADIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88	339.88	10.98	04/2014	03/2016	23	-
27	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01	365.01	6.56	06/2015	03/2016	9	-
28	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45	289.45	97.48	05/2014	10/2016	29	-
29	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82	269.82	40.12	04/2014	11/2016	31	-
30	ASHOK EXPN OCP CCL (10 MTY) - [N060100096]CCL,JHARKHAND	12/2007	341.63	341.63	124.95	03/2011	03/2017	72	-
31	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL	11/2006	287.18	287.18	225.39	03/2011	03/2017	72	-
32	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]JNCL,MADHYA PRADESH	10/2007	259.40	259.40	25.10	03/2012	03/2017	60	-
33	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77	457.77	181.15	03/2013	03/2017	48	-
34	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08	172.08	148.48	03/2010	03/2017	84	-
35	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63	453.63	99.71	12/2012	03/2017	51	-
36	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28	207.28	191.76	03/2012	03/2017	60	-
37	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53	479.63	173.59	03/2013	03/2017	48	-
38	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87	179.87	-	03/2012	03/2017	60	-
39	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46	162.46	-	03/2014	03/2017	36	-
40	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33	417.33	13.78	07/2016	03/2017	8	-
41	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03	249.03	73.99	03/2012	03/2018	72	-
42	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29	242.29	0.03	03/2015	03/2018	36	-

(July 2015)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
43	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL, TELANGANA	07/2011	447.06	447.06	29.03	03/2015	03/2018	36	-
44	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL, TELANGANA	07/2011	162.76	162.76	1.31	03/2015	03/2019	48	-
45	TALABIRA OCP - [N06000043]MCL, ODISHA	03/2008	447.72	447.72	52.36	03/2016	03/2020	48	-
46	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL, CHHATISGARH	09/2008	152.43	152.43	24.72	03/2015	03/2020	60	-
47	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH	07/2008	178.44	178.44	0.30	03/2014	03/2020	72	-
48	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL, ODISHA	02/2008	395.87	395.87	76.74	03/2015	03/2021	72	-
	Total		24,021.72	28,029.86	18,170.02				
	<u>STEEL</u>								
49	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL, ODISHA	10/2012	160.48	160.48	132.35	09/2014	07/2015	10	-
50	CAPTIVE POWER PLANT - 2 - [N12000087]RINL, ANDHRA PRADESH	02/2011	677.00	677.00	523.82	09/2013	07/2015	22	-
51	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL, JHARKHAND	05/2010	6,325.00	6,325.00	5,164.71	12/2011	08/2015	44	-
52	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC, KARNATAKA	02/2011	898.55	898.55	390.19	05/2013 01/2015	08/2015	27	7
53	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODISHA - [N12000079]SAIL, ODISHA	06/2012	237.09	237.09	192.84	12/2014	09/2015	9	-
54	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHHATISGARH - [N12000078]SAIL, CHHATISGARH	07/2012	332.65	332.65	205.40	08/2014	11/2015	15	-
55	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL, MAHARASHTRA	12/2011	187.33	187.33	163.67	10/2013	12/2015	26	-
56	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]SAIL, WEST BENGAL	11/2012	313.05	313.05	267.06	06/2015	12/2015	6	-
57	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, CHHATISGARH	08/2010	17,265.00	17,265.00	14,537.66	03/2013	03/2016	36	-
58	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL, ANDHRA PRADESH	07/2011	877.73	877.73	263.16	07/2015	03/2016	8	-
59	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL, ANDHRA PRADESH	05/2012	404.16	404.16	159.15	07/2015	03/2017	20	-
	Total		27,678.04	27,678.04	22,000.01				
	<u>PETROCHEMICALS</u>								
60	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, ASSAM	04/2006	5,460.61 8,920.00	9,833.52	8,784.45	04/2012 12/2013	09/2015	41	21

(July 2015)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	Total		5,460.61	9,833.52	8,784.45				
	<u>PETROLEUM</u>								
61	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	12/2012	607.06	607.06	57.94	01/2016	04/2017	15	-
62	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]ONGC,MAHARASHTRA	03/2012	5,608.40	5,608.40	4,456.55	05/2015	08/2015	3	3
63	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL,MAHARASHTRA	03/2012	1,419.00	1,419.00	1,205.72	12/2014	08/2015	8	-
64	102 MW WIND POWER PROJECT - [N16000119]ONGC,RAJASTHAN	07/2010	1,106.00	678.02	405.00	06/2012	09/2015	39	6
65	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL,TAMIL NADU	12/2012	279.00	279.00	160.87	12/2014	09/2015	9	-
66	PARADIP REFINERY PROJECT - [N16000058]IOCL,ODISHA	02/2009	29,777.00	34,555.00	29,606.96	11/2012	10/2015	35	23
67	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL,ODISHA	07/2009	199.75	239.73	192.28	07/2013	10/2015	27	-
68	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA	12/2009	1,584.00	1,584.00	1,262.55	08/2015	12/2015	4	-
69	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79	1,256.72	896.92	05/2013	12/2015	31	18
70	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,MULTI STATE	08/2011	586.00	586.00	342.83	08/2015	12/2015	4	-
71	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50	686.58	478.03	04/2015	12/2015	8	8
72	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96	191.96	92.09	05/2015	12/2015	7	-
73	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00	1,227.00	979.86	10/2011	01/2016	51	-
74	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA	01/2006	993.00	1,693.00	1,427.40	01/2012	01/2016	48	-
75	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00	1,793.00	1,173.22	09/2012	03/2016	42	-
76	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32	463.32	283.90	06/2011	03/2016	57	48
77	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17	600.17	375.14	12/2014	05/2016	17	12
78	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00	913.00	424.47	08/2015	06/2016	10	-

(July 2015)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
79	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL, ASSAM	09/2012	871.35 -	1,200.00	281.58	03/2015 11/2015	06/2016	15	7
80	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]IOCL, BIHAR	04/2013	480.00 -	480.00	44.48	02/2016 -	07/2016	5	-
81	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, ASSAM	03/2009	2,465.15 2,378.89	2,378.89	1,781.40	03/2013 03/2016	03/2017	48	12
82	AHMEDABAD REDEVELOPMENT PROJECT - [N16000120]ONGC, GUJARAT	11/2010	1,916.10 -	1,916.10	1,161.74	12/2014 -	12/2017	36	-
83	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC, MULTI STATE	05/2013	4,124.35 -	4,124.35	75.24	04/2016 04/2016	12/2017	20	20
84	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL, WEST BENGAL	03/2014	3,076.00 -	3,076.00	98.00	09/2017 -	12/2017	3	-
85	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL, MULTI STATE	07/2009	3,957.00 3,561.00	3,561.00	5.92	01/2013 -	12/2018	71	-
86	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC, GUJARAT	11/2010	2,189.63 -	2,189.63	1,035.48	12/2014 -	12/2018	48	-
	Total		67,932.53 -	73,306.93	48,305.57				
	<u>POWER</u>								
87	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO, TRIPURA	07/2009	421.01 1,007.68	1,007.68	902.86	07/2013 -	08/2015	25	-
88	TRANSMISSION SYSTEM OF VINDDHUACHAL - IV AND RIHAND - III GEN. PROJ. - [N18000076]PGCIL, MULTI STATE	03/2010	4,672.99 -	4,672.99	3,756.67	11/2012 -	08/2015	33	-
89	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJ. IN ORISSA PART-C - [N18000096]PGCIL, MULTI STATE	03/2011	2,569.25 3,105.51	3,105.51	2,854.67	03/2014 06/2015	08/2015	17	2
90	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL, MADHYA PRADESH	03/2012	213.78 -	213.78	201.04	03/2014 -	08/2015	17	-
91	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL, MULTI STATE	09/2012	1,508.74 -	1,508.74	950.08	03/2015 -	09/2015	6	-
92	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL, ODISHA	12/2010	2,743.19 -	2,743.19	2,783.30	12/2013 -	09/2015	21	-
93	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN. PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL, MULTI STATE	05/2010	250.03 -	250.03	142.10	01/2013 -	09/2015	32	-
94	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL, MULTI STATE	12/2011	2,422.66 -	2,422.66	2,085.56	08/2014 -	09/2015	13	-

(July 2015)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
95	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL, GUJARAT	12/2011	552.44 -	552.44	529.30	02/2014 -	09/2015	19	-
96	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL, MULTI STATE	02/2012	1,927.16 -	1,927.16	1,533.67	10/2014 -	09/2015	11	-
97	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL, MULTI STATE	09/2012	524.40 -	524.40	194.52	04/2015 -	09/2015	5	-
98	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL, ODISHA	09/2010	2,074.86 2,348.37	2,348.37	1,878.34	03/2013 06/2015	10/2015	31	4
99	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL, MULTI STATE	07/2010	752.64 689.03	689.03	490.72	07/2013 05/2015	11/2015	28	6
100	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL, MULTI STATE	10/2011	487.49 -	487.49	379.02	06/2014 -	11/2015	17	-
101	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL, KARNATAKA	03/2005	1,007.16 -	1,007.16	1,002.91	12/2007 12/2009	12/2015	96	72
102	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL, MULTI STATE	03/2011	1,585.12 -	1,585.12	1,492.46	11/2013 -	12/2015	25	-
103	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL, JHARKHAND	10/2011	558.26 -	558.26	464.61	11/2013 -	12/2015	25	-
104	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL, MULTI STATE	12/2011	297.33 346.79	346.79	285.47	08/2014 06/2015	12/2015	16	6
105	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL, MULTI STATE	11/2011	723.63 -	723.63	526.22	11/2014 -	12/2015	13	-
106	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL, TAMIL NADU	05/2005	1,779.29 2,159.07	2,159.07	1,894.05	09/2008 03/2012	03/2016	90	48
107	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL, MAHARASHTRA	12/2007	477.69 721.81	721.81	521.59	09/2010 06/2013	03/2016	66	33
108	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO, ARUNACHAL PRADESH	12/2008	573.99 1,487.49	1,487.49	1,016.43	08/2013 -	03/2016	31	-
109	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL, MULTI STATE	02/2009	509.66 -	509.66	468.66	11/2011 -	03/2016	52	-
110	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL, MULTI STATE	02/2009	410.29 -	410.29	331.57	02/2012 -	03/2016	49	-
111	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL, MULTI STATE	10/2008	4,824.12 -	4,824.12	4,133.98	10/2012 -	03/2016	41	-
112	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL, WEST BENGAL	04/2010	4,404.57 -	4,404.57	1,959.15	01/2015 -	03/2016	14	-

(July 2015)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
113	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	2,176.10	12/2012 -	03/2016	39	-
114	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,056.29	08/2012 -	03/2016	43	-
115	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	739.34	11/2012 -	03/2016	40	-
116	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,318.22	04/2013 -	03/2016	35	-
117	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHHATTISGARH - [N18000112]PGCIL,CHHATTISGARH	11/2011	2,127.51 -	2,127.51	2,211.93	07/2014 -	03/2016	20	-
118	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHHATTISGARH - [N18000116]PGCIL,CHHATTISGARH	12/2011	1,746.65 2,228.71	2,228.71	1,265.43	08/2014 12/2015	03/2016	19	3
119	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATTISGARH	01/2012	1,422.85 -	1,422.85	1,181.42	01/2015 -	03/2016	14	-
120	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	2,456.41	10/2014 -	03/2016	17	-
121	KBUNL-MUZAFFARPUR TPP STAGE-II-SUBSIDIARY (2X195 MW) - [N18000191]NTPC,BIHAR	03/2010	3,984.03 -	3,984.03	2,916.06	01/2013 -	03/2016	38	-
122	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]NHPC,WEST BENGAL	09/2005	1,061.38 -	1,929.15	1,813.21	09/2009 -	06/2016	81	-
123	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATTISGARH	05/2011	1,961.87 -	1,961.87	1,724.75	05/2014 -	06/2016	25	-
124	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,826.86	09/2014 -	06/2016	21	-
125	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	77.53	09/2014 -	06/2016	21	-
126	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATTISGARH	03/2012	9,569.76 -	9,569.76	4,720.39	06/2015 -	06/2016	12	-
127	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	844.85	12/2015 -	06/2016	6	-
128	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	240.70	06/2015 -	08/2016	14	-

(July 2015)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
129	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	791.33	06/2015 -	08/2016	14	-
130	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM	07/1998	368.72 1,381.71	1,381.71	857.94	07/2006 12/2015	10/2016	123	10
131	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,497.72	4,056.08	01/2016 -	11/2016	10	-
132	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	-	04/2016 -	11/2016	7	-
133	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	11,005.30	08/2013 -	12/2016	40	-
134	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	1,127.43	11/2012 -	12/2016	49	-
135	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 6,749.18	6,749.18	5,365.00	09/2011 -	03/2017	66	-
136	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	5,353.00	4,753.79	05/2014 -	06/2017	37	-
137	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	5,138.00	11/2016 -	08/2017	9	-
138	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 -	195.42	29.03	02/2014 -	09/2017	43	-
139	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	3,530.14	12/2016 -	09/2017	9	-
140	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 15,095.67	15,095.67	10,764.00	01/2011 10/2014	03/2018	86	41
141	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	1,335.62	07/2010 02/2016	05/2018	94	27
142	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	7,818.68	5,142.86	09/2009 -	12/2018	111	-
143	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	2,512.00	03/2013 -	12/2018	69	-
144	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	3,745.08	701.40	06/2013 -	12/2019	78	-
	Total		142,026.14 -	165,283.13	116,458.36				
	HEAVY INDUSTRY								
145	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]HIPE,MULTI STATE	04/2011	1,718.00 -	3,827.30	-	09/2011 -	12/2017	75	-
	Total		1,718.00 -	3,827.30	.00				
	RAILWAYS								
146	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	874.57	730.11	03/2013 -	09/2015	30	-

(July 2015)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
147	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL	04/1999	207.52 -	207.52	223.44	12/2012 -	09/2015	33	-
148	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR, BIHAR	04/2002	921.00 -	2,363.00	1,691.12	03/2009 12/2012	10/2015	79	34
149	ETAWAH-MAINPURI (NL), NCR - [220100318]NCR, UTTAR PRADESH	04/1997	120.00 245.39	245.39	249.33	12/2008 -	10/2015	82	-
150	RANCHI-LOHARDAGA (GC), SER - [220100214]SER, JHARKHAND	04/1997	194.07 -	335.00	230.67	06/2004 -	12/2015	138	-
151	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR, BIHAR	04/2001	624.47 -	2,921.00	2,521.72	10/2007 12/2012	12/2015	98	36
152	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, MADHYA PRADESH	09/2007	687.20 -	800.00	793.71	03/2010 -	12/2015	69	-
153	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP) - [220100164]MRTP, MAHARASHTRA	03/1996	495.44 495.44	1,781.98	440.08	03/2004 12/2010	03/2016	144	63
154	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE, UTTAR PRADESH	02/2008	171.10 236.37	275.08	141.55	03/2012 12/2013	03/2016	48	27
155	KATAKHAL TO BHAIRABI - [N22000126]NFR, ASSAM	04/1998	227.90 200.00	331.40	182.22	12/2012 -	03/2016	39	-
156	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR, ASSAM	04/1996	1,676.31 -	5,500.00	4,734.45	03/2009 -	03/2016	84	-
157	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER, JHARKHAND	04/2010	309.44 388.67	583.00	144.66	12/2015 -	03/2016	3	-
158	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR, TRIPURA	04/1999	895.00 575.00	1,242.25	1,005.81	03/2007 -	03/2016	108	-
159	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	204.56	03/2016 -	06/2016	3	-
160	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER, ODISHA	04/2010	149.90 -	230.00	68.67	03/2015 -	12/2016	21	-
161	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	714.10	65.93	04/2016 -	03/2017	11	-
162	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR, ASSAM	09/1997	1,500.00 1,000.00	4,996.19	3,410.06	04/2008 03/2014	06/2017	110	39
163	KATIHAR - JOGBANI (GC) (NEFR) - [220100247]NFR, BIHAR	09/2001	492.98 -	1,727.27	743.74	12/2010 -	03/2018	87	-
164	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	733.00 733.00	2,531.34	1,732.43	12/2008 -	03/2018	111	-
165	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA	04/2008	813.34 813.34	2,876.00	823.83	03/2014 -	03/2018	48	-
166	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	619.34 619.34	2,820.25	199.31	04/2014 03/2015	03/2018	47	36
167	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	4,874.58	1,911.65	03/2016 -	06/2018	27	-
168	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	19,565.00	10,658.34	11/2002 -	12/2018	193	-

(July 2015)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
169	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 727.56	6,570.75	2,787.99	03/2011 03/2014	03/2019	96	60
170	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,157.54	1,544.40	590.26	03/1998 -	12/2019	261	-
171	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,WEST BENGAL	03/1998	111.90 1,039.29	2,371.85	486.25	03/2005 12/2008	12/2019	177	132
172	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 1,013.74	1,428.00	466.36	06/2005 07/2011	12/2019	174	101
173	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 1,339.48	4,190.00	88.56	12/2015 -	03/2020	51	-
	Total		24,665.62 -	76,297.64	37,326.81				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
174	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	624.00	-	04/2014 -	07/2015	15	-
175	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	909.00	982.90	05/2014 -	07/2015	14	-
176	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	201.66	191.80	09/2008 -	09/2015	84	-
177	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	398.00	344.40	02/2014 -	09/2015	19	-
178	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	2,388.00	2,301.00	06/2014 -	11/2015	17	-
179	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.00 -	280.13	173.80	11/2008 -	12/2015	85	-
180	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	209.00	11.28	01/2013 -	12/2015	35	-
181	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00 -	1,232.00	590.90	08/2015 -	02/2016	6	-
182	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	1,047.00	295.70	06/2014 -	03/2016	21	-
183	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19 -	484.19	285.50	10/2014 -	03/2016	17	-
184	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	929.60	09/2014 -	06/2016	21	-
185	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	1,693.75	2,762.00	08/2011 -	09/2016	61	-
186	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2016	35	-
187	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,138.00	03/2014 -	04/2017	37	-
	Total		14,138.98 -	14,310.73	10,244.48				
	<u>SHIPPING AND PORTS</u>								

(July 2015)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
188	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU, MAHARASHTRA	01/2007	366.39 669.46	669.46	407.32	12/2010 -	01/2016	61	-
	Total		366.39 -	669.46	407.32				
	<u>TELECOMMUNICATIONS</u>								
189	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL, MULTI STATE	10/2009	384.00 -	384.00	66.02	10/2010 08/2015	09/2015	59	1
	Total		384.00 -	384.00	66.02				
	<u>URBAN DEVELOPMENT</u>								
190	FARIDABAD EXTENSION - [N28000057]DMRCL, DELHI	09/2011	2,494.00 -	2,494.00	1,272.44	09/2014 -	08/2015	11	-
191	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD, ODISHA	11/2012	238.43 -	238.43	-	02/2015 -	08/2015	6	-
192	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASHTRA - [N28000074]CPWD, MAHARASHTRA	12/2012	315.00 -	315.00	3.11	06/2015 -	08/2015	2	-
193	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD, HIMACHAL PRADESH	11/2012	270.83 -	270.83	-	11/2014 -	10/2015	11	-
194	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD, DELHI	05/2009	261.85 -	261.85	6.26	05/2013 -	11/2015	30	-
195	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL, MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	12/2015	11	-
196	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD, DELHI	05/2012	405.01 -	405.01	-	12/2014 -	04/2016	16	-
197	2000 BOYS HOSTEL (1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD, JHARKHAND	09/2012	171.86 -	171.86	-	03/2016 -	05/2016	2	-
198	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL, TAMIL NADU	02/2009	14,600.00 14,600.00	14,600.00	10,826.56	12/2015 -	08/2016	8	-
199	DELHI MRTS PHASE-III - [N28000056]DMRCL, DELHI	09/2011	38,585.00 -	38,585.00	16,432.68	03/2016 -	12/2016	9	-
200	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD, MADHYA PRADESH	12/2012	188.87 -	188.87	5.79	12/2014 -	12/2016	24	-
201	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD, WEST BENGAL	02/2014	156.57 -	156.57	-	09/2015 -	12/2016	15	-

(July 2015)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
202	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD, DELHI	07/2012	884.30 -	884.30	-	08/2014 -	06/2017	34	-
	Total		81,707.72 -	81,707.72	28,546.84				
	Grand Total		428,028.81	523,419.89	323,370.51				

LIST OF ROAD SECTOR PROJECTS IMPLEMENTED BY NHAI AS ON 31.07.2015 FOR WHICH DATE OF COMMISSIONING HAS EXPIRED/LAPSED							
All cost in Rs Crore							
S. No.	PROJECT	DOA	DOC ORIGINAL	STATE NAME	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED
1	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15)	5 / 2009	10/2011	ANDHRA PRADESH	0 / 0	572.30	572.30
2	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM	11 / 2010	5/2013	ANDHRA PRADESH	0 / 0	1585.00	1585.00
3	TIRUPATI - TIRUTHANI - CHENNAI	4 / 2011	10/2013	ANDHRA PRADESH	0 / 0	571.00	571.00
4	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	11 / 2011	5/2014	ANDHRA PRADESH	0 / 0	1535.00	1535.00
5	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54	12 / 2003	9/2007	ASSAM	0 / 0	212.00	212.00
6	HARANGAJO TO MAIBANG, NH-54	12 / 2003	7/2009	ASSAM	0 / 0	196.00	331.23
7	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12 / 2003	4/2009	ASSAM	0 / 0	199.81	385.13
8	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	12 / 2003	4/2009	ASSAM	0 / 0	200.00	200.00
9	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	12 / 2003	6/2008	ASSAM	0 / 0	195.00	195.00
10	NAGAON TO DHARAMTUL (AS-2)	12 / 2003	6/2008	ASSAM	0 / 0	264.72	264.72
11	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	12 / 2003	6/2008	ASSAM	0 / 0	237.80	237.80
12	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C	12 / 2003	6/2005	ASSAM	0 / 0	230.00	230.00
13	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12 / 2003	11/2008	ASSAM	0 / 0	167.64	167.64
14	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12 / 2003	2/2009	ASSAM	0 / 0	280.00	361.00
15	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	12 / 2003	9/2008	BIHAR	0 / 0	332.94	332.94
16	PATNA-MUZZAFFARPUR	8 / 2010	2/2013	BIHAR	0 / 0	671.30	671.30
17	2-LANNING WITH PS KHAGARIA-PURNEA	5 / 2011	2/2014	BIHAR	0 / 0	664.00	664.00
18	2 LANNING OF MOKAMA-MUNGER	5 / 2011	5/2013	BIHAR	0 / 0	351.54	351.54
19	2-LANING WITH PAVED SHOULDER OF MUZZAFFARPUR-BARAUNI	7 / 2012	7/2014	BIHAR	0 / 0	356.40	356.40
20	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	9 / 2011	3/2014	BIHAR	0 / 0	574.00	574.00
21	4-LANNING OF CHAPRA-HAJIPUR	1 / 2011	7/2013	BIHAR	0 / 0	575.00	575.00
22	2 LANNING OF MUZZAFFARPUR - SONBARSA	5 / 2011	11/2013	BIHAR	0 / 0	511.54	511.54
23	2-LANNING WITH PS MOTIHARI-RAXAUL	10 / 2011	4/2014	BIHAR	0 / 0	375.09	375.09
24	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	3 / 2010	9/2012	GUJARAT	0 / 0	1509.10	1509.10
25	4 LANNING OF GODHARA TO GUJARAT/MP BORDER	3 / 2011	8/2013	GUJARAT	0 / 0	785.50	785.50
26	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6	3 / 2012	9/2014	GUJARAT	0 / 0	828.00	828.00
27	KANDLA - MUNDRA PORT	1 / 2011	7/2013	GUJARAT	0 / 0	953.88	953.88
28	SAMAIKHIALI - GANDHIDHAM	9 / 2010	3/2013	GUJARAT	0 / 0	805.39	805.39
29	4 LANNING OF AHMEDABAD TO GODHARA	12 / 2010	6/2013	GUJARAT	0 / 0	1008.50	1008.50
30	DELHI/ HARYANA BORDER TO ROHTAK	4 / 2007	5/2010	HARYANA	0 / 0	486.00	486.00
31	ROHTAK-BAWAL	5 / 2011	11/2013	HARYANA	0 / 0	650.00	650.00

32	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	5 / 2009	11/2011	HARYANA	0 / 0	1108.00	2288.00
33	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	7 / 2010	7/2015	JAMMU AND KASHMIR	0 / 0	1987.00	1987.00
34	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	7 / 2010	7/2013	JAMMU AND KASHMIR	0 / 0	1813.76	1813.76
35	NASHRI- CHANANI	5 / 2011	6/2015	JAMMU AND KASHMIR	0 / 0	2159.00	2159.00
36	SRINAGAR TO BANIHAL	6 / 2011	6/2014	JAMMU AND KASHMIR	0 / 0	1100.70	1100.70
37	DEVIHALLI-HASSAN	12 / 2010	/	KARNATAKA	0 / 0	453.00	453.00
38	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER	3 / 2011	9/2013	KARNATAKA	0 / 0	359.00	359.00
39	BELGAUM-DHARWAD(NH-4)	12 / 2010	/	KARNATAKA	0 / 0	480.00	480.00
40	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION	4 / 2011	10/2013	KERALA	0 / 0	682.00	682.00
41	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM)	2 / 2010	8/2012	KERALA	0 / 0	617.00	617.00
42	INDORE-DEWAS(NH-3)	11 / 2010	5/2013	MADHYA PRADESH	0 / 0	325.00	325.00
43	INDORE-JHABUA-GUJRAT/MP	10 / 2010	4/2013	MADHYA PRADESH	0 / 0	1175.00	1175.00
44	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	3 / 2005	7/2012	MAHARASHTRA	0 / 0	940.00	940.00
45	PUNE-SATARA(NH-4)	10 / 2010	3/2013	MAHARASHTRA	0 / 0	1724.55	1724.55
46	TALEGAON-AMRAVATI	11 / 2009	11/2013	MAHARASHTRA	0 / 0	567.00	567.00
47	PUNE-SHOLAPUR,PKG-II	9 / 2011	1/2014	MAHARASHTRA	0 / 0	835.00	835.00
48	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	5 / 2013	2/2014	MAHARASHTRA	0 / 0	1348.20	1348.20
49	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM)	2 / 2011	11/2012	MAHARASHTRA	0 / 0	193.45	193.45
50	JORBAT - BARAPANI	1 / 2011	1/2014	MEGHALAYA	0 / 0	536.00	536.00
51	GWALIOR-JHANSI, NH-75	12 / 2003	12/2009	MULTI STATE	0 / 0	604.00	604.00
52	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM)	4 / 2012	4/2014	MULTI STATE	0 / 0	624.00	624.00
53	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	12 / 2003	9/2010	MULTI STATE	0 / 0	232.45	232.45
54	DELHI AGRA APPROVED LENGTH 180.0 KM	10 / 2012	4/2015	MULTI STATE	4 / 2015	1928.22	1928.22
55	4-LANING OF FARAKA-RAIGANJ	2 / 2011	8/2013	MULTI STATE	0 / 0	1078.84	1078.84
56	RANCHI-RARGA-JAMSETHPUR	12 / 2012	6/2015	MULTI STATE	0 / 0	1479.00	1479.00
57	PANVEL-INDAPUR	12 / 2011	6/2014	MULTI STATE	0 / 0	942.69	942.69
58	4-LANING OF BRAHAMPORE-FARAKA	2 / 2011	8/2013	MULTI STATE	0 / 0	998.79	998.79
59	4-LANING OF RAIGANJ-DALKOLA	2 / 2011	8/2013	MULTI STATE	0 / 0	580.43	580.43
60	MUZAFFARNAGAR-HARIDWAR	9 / 2011	3/2013	MULTI STATE	0 / 0	754.00	754.00
61	4 LANING OF NAGPUR-BETUL	2 / 2011	8/2014	MULTI STATE	0 / 0	2498.76	2498.76
62	BHUBANESWAR TO PURI	3 / 2011	8/2013	ODISHA	0 / 0	500.29	500.29
63	CHAMBAL BRIDGE, NH-76 (RJ-5)	12 / 2003	2/2010	RAJASTHAN	0 / 0	275.00	281.31
64	REENGUS SIKAR	3 / 2012	9/2014	RAJASTHAN	0 / 0	333.51	333.51
65	JAIPUR-REENGUS	8 / 2010	2/2013	RAJASTHAN	0 / 0	267.81	267.81
66	KOTA BYPASS,RJ-4, NH-76 (NHAI)	12 / 2003	10/2008	RAJASTHAN	0 / 0	275.00	250.39
67	DEOLI-KOTA	1 / 2011	7/2013	RAJASTHAN	0 / 0	593.00	593.00
68	KISHANGARH-AJMER-BEAWER	11 / 2009	5/2012	RAJASTHAN	0 / 0	795.00	795.00
69	JAIPUR-TONK-DEOLI	6 / 2010	12/2012	RAJASTHAN	0 / 0	792.06	792.06
70	CHENNAI-TADA(SIX LANE)	4 / 2009	10/2011	TAMIL NADU	0 / 0	353.37	353.37
71	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	9 / 2011	12/2013	TAMIL NADU	0 / 0	1250.00	1250.00

72	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI	9 / 2011	8/2013	TAMIL NADU	0 / 0	485.00	485.00
73	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS	5 / 2010	5/2013	TAMIL NADU	0 / 0	374.00	374.00
74	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI ENNORE PORT CONNECTIVITY	6 / 2011	6/2013	TAMIL NADU	0 / 0	600.00	600.00
75	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT- MADURAVOYAL NH NO.4	9 / 2010	9/2013	TAMIL NADU	0 / 0	1655.00	1655.00
76	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00	6 / 2011	12/2013	TAMIL NADU	0 / 0	535.00	535.00
77	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	9 / 2010	3/2013	TAMIL NADU	0 / 0	852.00	852.00
78	MURADABAD-BAREILY	4 / 2010	6/2013	UTTAR PRADESH	0 / 0	1267.00	1267.00
79	2 LANING WITH PS KANPUR KABRAI	1 / 2013	7/2014	UTTAR PRADESH	0 / 0	373.47	373.47
80	GHAZIABAD-ALIGARH NH-91	2 / 2011	8/2013	UTTAR PRADESH	0 / 0	1141.00	1141.00
81	BAREILY-SITAPUR (NH-24)	3 / 2011	9/2013	UTTAR PRADESH	0 / 0	1046.00	1046.00
82	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	7 / 2012	1/2014	UTTAR PRADESH	0 / 0	291.36	291.36
83	HARIDWAR-DEHRADUN (APPROVED LENGTH 69)	11 / 2011	10/2013	UTTARAKHAND	0 / 0	478.00	478.00
84	6-LANING OF DHANKUNI-KHARAGPUR SECTION	4 / 2012	9/2014	WEST BENGAL	0 / 0	1396.18	1396.18
85	BARSAT-KRISHNANAGAR	8 / 2012	2/2015	WEST BENGAL	0 / 0	867.00	867.00
86	KRISHNANAGAR-BERHAMPUR	2 / 2012	7/2014	WEST BENGAL	0 / 0	702.16	702.16

LIST OF ROAD SECTOR PROJECTS IMPLEMENTED BY NHAI AS ON 31.07.2015 FOR WHICH CUMULATIVE EXPENDITURE HAS BEEN REPORTED ZERO								
All cost in Rs Crore								
S. No.	PROJECT NAME	DOA	DOC ORIGINAL	STATE NAME	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15)	5 / 2009	10/2011	ANDHRA PRADESH	0 / 0	572.30	572.30	0.00
2	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM	11 / 2010	5/2013	ANDHRA PRADESH	0 / 0	1585.00	1585.00	0.00
3	TIRUPATI - TIRUTHANI - CHENNAI	4 / 2011	10/2013	ANDHRA PRADESH	0 / 0	571.00	571.00	0.00
4	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	11 / 2011	5/2014	ANDHRA PRADESH	0 / 0	1535.00	1535.00	0.00
5	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54	12 / 2003	9/2007	ASSAM	0 / 0	212.00	212.00	0.00
6	HARANGAJO TO MAIBANG, NH-54	12 / 2003	7/2009	ASSAM	0 / 0	196.00	331.23	0.00
7	BRAHMPUTRA BRIDGE, NH NO-31	12 / 2003	4/2010	ASSAM	1 / 2016	217.61	309.56	0.00
8	SONAPUR TO GUWAHTI (AS-3)	12 / 2003	3/2008	ASSAM	1 / 2016	245.00	245.00	0.00
9	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	12 / 2003	5/2008	ASSAM	10 / 2015	160.00	160.00	0.00
10	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12 / 2003	4/2009	ASSAM	0 / 0	199.81	385.13	0.00
11	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	12 / 2003	4/2009	ASSAM	0 / 0	200.00	200.00	0.00
12	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	12 / 2003	6/2008	ASSAM	0 / 0	195.00	195.00	0.00
13	GUWHATI TO NALBARI (AS-4)	12 / 2003	4/2008	ASSAM	8 / 2015	175.96	175.96	0.00
14	NALBARI TO BIJNI (AS-6)	12 / 2003	6/2008	ASSAM	8 / 2015	225.00	225.00	0.00
15	NAGAON TO DHARAMTUL (AS-2)	12 / 2003	6/2008	ASSAM	0 / 0	264.72	264.72	0.00
16	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	12 / 2003	6/2008	ASSAM	0 / 0	237.80	237.80	0.00
17	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C	12 / 2003	6/2005	ASSAM	0 / 0	230.00	230.00	0.00
18	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12 / 2003	11/2008	ASSAM	0 / 0	167.64	167.64	0.00
19	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12 / 2003	2/2009	ASSAM	0 / 0	280.00	361.00	0.00
20	NALBARI T BIJNI (AS-7)	12 / 2003	4/2008	ASSAM	1 / 2016	208.00	208.00	0.00
21	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	12 / 2003	9/2008	BIHAR	0 / 0	332.94	332.94	0.00
22	PATNA-MUZZAFFARPUR	8 / 2010	2/2013	BIHAR	0 / 0	671.30	671.30	0.00
23	2-LANNING WITH PS KHAGARIA-PURNEA	5 / 2011	2/2014	BIHAR	0 / 0	664.00	664.00	0.00
24	2 LANNING OF MOKAMA-MUNGER	5 / 2011	5/2013	BIHAR	0 / 0	351.54	351.54	0.00
25	2-LANING WITH PAVED SHOULDER OF MUZZAFFARPUR-BARAUNI	7 / 2012	7/2014	BIHAR	0 / 0	356.40	356.40	0.00
26	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	9 / 2011	3/2014	BIHAR	0 / 0	574.00	574.00	0.00
27	4-LANNING OF CHAPRA-HAJIPUR	1 / 2011	7/2013	BIHAR	0 / 0	575.00	575.00	0.00
28	2 LANNING OF MUZZAFFARPUR - SONBARSA	5 / 2011	11/2013	BIHAR	0 / 0	511.54	511.54	0.00
29	2-LANNING WITH PS MOTIHARI-RAXAUL	10 / 2011	4/2014	BIHAR	0 / 0	375.09	375.09	0.00
30	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	3 / 2010	9/2012	GUJARAT	0 / 0	1509.10	1509.10	0.00
31	4 LANNING OF GODHARA TO GUJARAT/MP BORDER	3 / 2011	8/2013	GUJARAT	0 / 0	785.50	785.50	0.00
32	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6	3 / 2012	9/2014	GUJARAT	0 / 0	828.00	828.00	0.00
33	KANDLA - MUNDRA PORT	1 / 2011	7/2013	GUJARAT	0 / 0	953.88	953.88	0.00
34	SAMAIKHALI - GANDHIDHAM	9 / 2010	3/2013	GUJARAT	0 / 0	805.39	805.39	0.00
35	4 LANNING OF AHMEDABAD TO GODHARA	12 / 2010	6/2013	GUJARAT	0 / 0	1008.50	1008.50	0.00

36	DELHI/ HARYANA BORDER TO ROHTAK	4 / 2007	5/2010	HARYANA	0 / 0	486.00	486.00	0.00
37	4-LANING OF ROHTAK JIND(LENGTH 45 KM)	10 / 2013	10/2015	HARYANA	10 / 2015	283.25	283.25	0.00
38	ROHTAK-BAWAL	5 / 2011	11/2013	HARYANA	0 / 0	650.00	650.00	0.00
39	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	5 / 2009	11/2011	HARYANA	0 / 0	1108.00	2288.00	0.00
40	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM)	11 / 2013	11/2016	HIMACHAL PRADESH	11 / 2016	1916.79	1916.79	0.00
41	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	7 / 2010	7/2015	JAMMU AND KASHMIR	0 / 0	1987.00	1987.00	0.00
42	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	7 / 2010	7/2013	JAMMU AND KASHMIR	0 / 0	1813.76	1813.76	0.00
43	NASHRI- CHANANI	5 / 2011	6/2015	JAMMU AND KASHMIR	0 / 0	2159.00	2159.00	0.00
44	SRINAGAR TO BANIHAL	6 / 2011	6/2014	JAMMU AND KASHMIR	0 / 0	1100.70	1100.70	0.00
45	DEVIHALLI-HASSAN	12 / 2010	/	KARNATAKA	0 / 0	453.00	453.00	0.00
46	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER	3 / 2011	9/2013	KARNATAKA	0 / 0	359.00	359.00	0.00
47	BELGAUM-DHARWAD(NH-4)	12 / 2010	/	KARNATAKA	0 / 0	480.00	480.00	0.00
48	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION	4 / 2011	10/2013	KERALA	0 / 0	682.00	682.00	0.00
49	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM)	2 / 2010	8/2012	KERALA	0 / 0	617.00	617.00	0.00
50	INDORE-DEWAS(NH-3)	11 / 2010	5/2013	MADHYA PRADESH	0 / 0	325.00	325.00	0.00
51	INDORE-JHABUA-GUJRAT/MP	10 / 2010	4/2013	MADHYA PRADESH	0 / 0	1175.00	1175.00	0.00
52	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	3 / 2005	7/2012	MAHARASHTRA	0 / 0	940.00	940.00	0.00
53	PUNE-SATARA(NH-4)	10 / 2010	3/2013	MAHARASHTRA	0 / 0	1724.55	1724.55	0.00
54	TALEGAON-AMRAVATI	11 / 2009	11/2013	MAHARASHTRA	0 / 0	567.00	567.00	0.00
55	PUNE-SHOLAPUR,PKG-II	9 / 2011	1/2014	MAHARASHTRA	0 / 0	835.00	835.00	0.00
56	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	5 / 2013	2/2014	MAHARASHTRA	0 / 0	1348.20	1348.20	0.00
57	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM)	2 / 2011	11/2012	MAHARASHTRA	0 / 0	193.45	193.45	0.00
58	JORBAT - BARAPANI	1 / 2011	1/2014	MEGHALAYA	0 / 0	536.00	536.00	0.00
59	GWALIOR-JHANSI, NH-75	12 / 2003	12/2009	MULTI STATE	0 / 0	604.00	604.00	0.00
60	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM)	4 / 2012	4/2014	MULTI STATE	0 / 0	624.00	624.00	0.00
61	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	12 / 2003	9/2010	MULTI STATE	0 / 0	232.45	232.45	0.00
62	DELHI AGRA APPROVED LENGTH 180.0 KM	10 / 2012	4/2015	MULTI STATE	4 / 2015	1928.22	1928.22	0.00
63	4-LANING OF FARAKA-RAIGANJ	2 / 2011	8/2013	MULTI STATE	0 / 0	1078.84	1078.84	0.00
64	RANCHI-RARGA-JAMSETHPUR	12 / 2012	6/2015	MULTI STATE	0 / 0	1479.00	1479.00	0.00
65	PANVEL-INDAPUR	12 / 2011	6/2014	MULTI STATE	0 / 0	942.69	942.69	0.00
66	4-LANING OF BRAHAMPORE-FARAKA	2 / 2011	8/2013	MULTI STATE	0 / 0	998.79	998.79	0.00
67	4-LANING OF RAIGANJ-DALKOLA	2 / 2011	8/2013	MULTI STATE	0 / 0	580.43	580.43	0.00
68	MUZAFFARNAGAR-HARIDWAR	9 / 2011	3/2013	MULTI STATE	0 / 0	754.00	754.00	0.00
69	4 LANING OF NAGPUR-BETUL	2 / 2011	8/2014	MULTI STATE	0 / 0	2498.76	2498.76	0.00
70	BHUBANESWAR TO PURI	3 / 2011	8/2013	ODISHA	0 / 0	500.29	500.29	0.00
71	CHAMBAL BRIDGE, NH-76 (RJ-5)	12 / 2003	2/2010	RAJASTHAN	0 / 0	275.00	281.31	0.00
72	REENGUS SIKAR	3 / 2012	9/2014	RAJASTHAN	0 / 0	333.51	333.51	0.00
73	JAIPUR-REENGUS	8 / 2010	2/2013	RAJASTHAN	0 / 0	267.81	267.81	0.00
74	KOTA BYPASS,RJ-4, NH-76 (NHAI)	12 / 2003	10/2008	RAJASTHAN	0 / 0	275.00	250.39	0.00
75	DEOLI-KOTA	1 / 2011	7/2013	RAJASTHAN	0 / 0	593.00	593.00	0.00
76	KISHANGARH-AJMER-BEAWER	11 / 2009	5/2012	RAJASTHAN	0 / 0	795.00	795.00	0.00
77	JAIPUR-TONK-DEOLI	6 / 2010	12/2012	RAJASTHAN	0 / 0	792.06	792.06	0.00
78	CHENNAI-TADA(SIX LANE)	4 / 2009	10/2011	TAMIL NADU	0 / 0	353.37	353.37	0.00

79	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	9 / 2011	12/2013	TAMIL NADU	0 / 0	1250.00	1250.00	0.00
80	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8	6 / 2013	11/2015	TAMIL NADU	11 / 2015	1287.95	1287.95	0.00
81	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI	9 / 2011	8/2013	TAMIL NADU	0 / 0	485.00	485.00	0.00
82	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS	5 / 2010	5/2013	TAMIL NADU	0 / 0	374.00	374.00	0.00
83	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	6 / 2011	6/2013	TAMIL NADU	0 / 0	600.00	600.00	0.00
84	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT- MADURAVOYAL NH NO.4	9 / 2010	9/2013	TAMIL NADU	0 / 0	1655.00	1655.00	0.00
85	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00	6 / 2011	12/2013	TAMIL NADU	0 / 0	535.00	535.00	0.00
86	CHENGAPALLI TO COIMBATORE BYPASS KM- 102.035-144.740 KM	9 / 2010	3/2013	TAMIL NADU	0 / 0	852.00	852.00	0.00
87	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	4 / 2014	9/2016	TELANGANA	9 / 2016	1266.60	1266.60	0.00
88	MURADABAD-BAREILY	4 / 2010	6/2013	UTTAR PRADESH	0 / 0	1267.00	1267.00	0.00
89	2 LANING WITH PS KANPUR KABRAI	1 / 2013	7/2014	UTTAR PRADESH	0 / 0	373.47	373.47	0.00
90	ETAWAH CHAKERI	3 / 2013	9/2015	UTTAR PRADESH	9 / 2015	1573.00	1573.00	0.00
91	GHAZIABAD-ALIGARH NH-91	2 / 2011	8/2013	UTTAR PRADESH	0 / 0	1141.00	1141.00	0.00
92	BAREILY-SITAPUR (NH-24)	3 / 2011	9/2013	UTTAR PRADESH	0 / 0	1046.00	1046.00	0.00
93	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	7 / 2012	1/2014	UTTAR PRADESH	0 / 0	291.36	291.36	0.00
94	HARIDWAR-DEHRADUN (APPROVED LENGTH 69)	11 / 2011	10/2013	UTTARAKHAND	0 / 0	478.00	478.00	0.00
95	6-LANING OF DHANKUNI-KHARAGPUR SECTION	4 / 2012	9/2014	WEST BENGAL	0 / 0	1396.18	1396.18	0.00
96	BARSAT-KRISHNANAGAR	8 / 2012	2/2015	WEST BENGAL	0 / 0	867.00	867.00	0.00
97	KRISHNANAGAR-BERHAMPUR	2 / 2012	7/2014	WEST BENGAL	0 / 0	702.16	702.16	0.00
