

**341st FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹ 150 crore and above)
March 2014**



NHPC - NIMOO BAZGO HYDROELECTRIC PROJECT



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India Ltd.
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead Travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised Catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Operation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petroleum Corporation Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative Ltd.
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation Ltd.
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Corporation.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Corporation.
NCL	Northern Coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation Ltd.
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corporation Ltd.
NGN	Next Generation Network
NLC	Neyveli Lignite Corporation Ltd.
NMDC	National Mineral Development Corporation Ltd.
NPC	Nuclear Power Corporation Ltd.
NRL	Numaligarh Refinery Ltd.
OB	Over Burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over Bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India Ltd.
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

Contents

Executive Summary in English	1 -9
Month wise list of completed projects Costing Rs. 150 Crore and Above During 2013-14	10-11
Summary of Projects	12-25
Trend and Graphical Analysis of Projects	26-38
Sector wise analysis of projects	39-39
List of All Ongoing Projects	40-70
Sector wise Graph	71-81
ANNEXURE	82-82
Central Sector Projects	83-83
List of Projects Having Expenditure More than cost	84-91
List of Projects Ahead of Schedule	92-92
List of Projects with out Original date of Commissioning	93-94
List of Projects with out date of Commissioning	95-106
List of On schedule Projects Original Schedule	107-113
List of Delayed Projects w.r.t Original Schedule	114-127
List of Projects Having Time and cost overrun w.r.t original	128-132
List of Projects Having cost overrun w.r.t original	133-144
List of Projects without Milestones	145-166
List of On schedule Projects w.r.t. Latest Schedule	167-174
List of Projects Ahead of Schedule w.r.t Latest Schedule	175-175
List of Delayed Projects w.r.t Latest Schedule	176-189

कार्यकारी सारांश

1. मार्च, 2014 की फ्लैश रिपोर्ट में ` 150 करोड़ और उससे अधिक लागत वाली केन्द्रीय क्षेत्र की 710 अवसंरचनात्मक परियोजनाओं की स्थिति दी गई है। मार्च, 2014 के दौरान 14 परियोजनाओं (8 परियोजनाएं पेट्रोलियम, 5 परियोजनाएं विद्युत तथा 1 परियोजना रेलवे क्षेत्र में है) के पूरा होने की सूचना दी गई है।

2. संदर्भाधीन माह के दौरान, 710 परियोजनाओं में से, 185 परियोजनाओं में नवीनतम समय-सारणी की तुलना में विलंब हुआ तथा 30 परियोजनाओं के संबंध में पिछले माह में सूचित की गई समापन की तारीख की तुलना में अतिरिक्त विलंब की सूचना दी गई है। इन 30 परियोजनाओं में से, 15 परियोजनाएं ` 1000 करोड़ और अधिक लागत वाली बड़ी परियोजनाएं हैं।

क्र.सं.	क्षेत्र	निगरानी के तहत आने वाली परियोजनाएं	नवीनतम समय-सारणी की तुलना में विलंबित परियोजनाएं	रिपोर्ट वाले माह के दौरान अतिरिक्त विलंबित परियोजनाएं	अतिरिक्त विलंबित बड़ी परियोजनाएं
1.	रेलवे	282	36	3	1
2.	सड़क परिवहन एवं राजमार्ग	132	7	1	0
3.	विद्युत	96	42	5	3
4.	पेट्रोलियम	76	48	14	9
5.	कोयला	56	29	1	1
6.	इस्पात	20	10	1	0
7.	पोत परिवहन एवं पत्तन	19	1	1	1
8.	दूरसंचार	10	4	3	0
9.	नागर विमानन	8	3	1	0
10.	शहरी विकास	5	1	0	0
11.	परमाणु ऊर्जा	4	4	0	0
12.	पेट्रोरसायन	1	0	0	0
13.	जल संसाधन	1	0	0	0
कुल		710	185	30	15

3. 710 परियोजनाओं के कार्यान्वयन की कुल मूल लागत लगभग ` 9,24,307.04 करोड़ थी तथा उनके पूरा होने की अनुमानित लागत ` 11,03,914.08 करोड़ रुपए होने की संभावना है जो 1,79,607.04 करोड़ (मूल लागत का 19.40%) की समग्र लागत वृद्धि को दर्शाता है। मार्च, 2014 तक इन परियोजनाओं पर किया गया व्यय ` 5,01,798.71 करोड़ है जो परियोजनाओं की अनुमानित लागत का 45.50% है। लागतवृद्धि की अधिकतम प्रतिशतता वाली 5 परियोजनाएं नीचे दी गई हैं:-

लागतवृद्धि की अधिकतम प्रतिशतता वाली 5 परियोजनाओं की सूची (31.03.2014 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (` करोड़)			लागत-वृद्धि (% में)
				मूल	संशोधित	अनुमानित	
1	नांगल बांध-तलवारा (एनएल), एनआर	रेलवे	03/1981	37.68	450.00	1036.78	2651.54
2	गाजोले-ईटाहार सहित इकलाखी से बलूरघाट तक नई बी जी लाइन रेलवे लाइन (एनएल) एनईएफआर	रेलवे	04/1983	36.80	274.41	703.17	1810.79
3	हावड़ा-आमता-चेपादंगा एनएल (एसईआर)	रेलवे	04/1974	31.42	393.46	535.40	1604.01
4	बांकुरा-दामोदर (जीसी) (एसईआर)	रेलवे	03/1998	111.90	1028.05	1423.98	1172.55
5	अकोला-खण्डवा जीसी अकोला-अकोट	रेलवे	04/2008	184.26	एन.आर.	2000.00	985.42

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

4. वास्तविक अर्थ में अधिकतम लागतवृद्धि वाली 5 परियोजनाएं निम्नानुसार हैं:-

अधिकतम लागतवृद्धि वाली 5 परियोजनाओं की सूची (31.03.2014 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (₹ करोड़)		
				मूल लागत	अनुमानित लागत	लागत-वृद्धि
1	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	2500.00	20000.00	17500.00
2	जिरीबाम से इंफाल (तुपु) (एनएल) (एनईएफआर)	रेलवे	04/2003	727.56	5996.00	5268.44
3	बंगलौर मेट्रो रेल परियोजना	शहरी विकास	05/2006	6395.33	11609.00	5214.00
4	सुबानश्री लोअर एचईपी (एनएचपीसी)	विद्युत	09/2003	6285.33	10667.00	4381.67
5	कुंडकुलम एपीपी (एनपीसीआईएल)	परमाणु ऊर्जा	12/2001	13171.00	17270.00	4099.00

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

5. 710 परियोजनाओं में से, 3 परियोजनाएं समय से पहले चल रही हैं, 156 समय पर तथा 185 परियोजनाएं नवीनतम समय-सारणी की तुलना में विलंबित हैं । तथापि, विलंबित परियोजनाओं की संख्या 209 तक और बढ़ जाती है यदि विलंब की गणना समापन की मूल समय-सारणी के आधार पर की जाती है । इसके अलावा, 23 परियोजनाएं किसी आरंभ संबंधी समय-सारणी/तारीख के बिना स्वीकृत की गई हैं तथा 343 परियोजनाओं के संबंध में न तो शुरू करने का वर्ष और न परियोजना के अंतरिम रूप से पूरा होने की अवधि सूचित की गई है । 185 विलंबित परियोजनाओं में से, 40 परियोजनाओं में 1 से 12 माह तक का विलंब हुआ, 43 परियोजनाओं में 13 से 24 महीने तक का विलंब हुआ, 63 परियोजनाओं में 25 से 60 माह तक का विलंब हुआ तथा 39 परियोजनाओं में 61 माह और उससे अधिक का विलंब हुआ । अधिकतम विलंब वाली 5 परियोजनाएं नीचे दी गई हैं:-

अधिकतम समयवृद्धि वाली 5 परियोजनाओं की सूची (31.03.2014 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	शुरू करने की तारीख		समय-वृद्धि (महीने में)
				मूल	अनुमानित	
1	फ्रेट आप्रेशनस इन्फोर्मेशन सिस्टम (एफओआईएस)	रेलवे	03/1984	03/1995	03/2015	240
2	गुना-इटावा बरास्ता शिवपुरी-ग्वालियर-भिंड एनएल (एनसीआर)	रेलवे	04/1986	03/1994	10/2013	238
3	लांझीगढ़-जूनागढ़ एनएल (ईसीओआर)	रेलवे	04/1993	03/2002	09/2013	143
4	बांकुरा-दामोदर (जीसी) (एसईआर)	रेलवे	03/1998	03/2005	12/2016	141
5	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	03/2001	12/2017	181

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक समयवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

6. विभिन्न अन्य परियोजना कार्यान्वयन एजेंसियों द्वारा यथा सूचित समयवृद्धि के संक्षिप्त कारणों में भूमि अधिग्रहण में विलंब, वन संबंधी अनुमति, उपस्करों की आपूर्ति में विलंब, निधि की कमी, भू वैज्ञानिक गतिविधियां, उपस्कर स्थापित करना, भूखनन की स्थिति, श्रम की कमी, ठेकेदार द्वारा अपर्याप्त संसाधन जुटाना, न्यायालय मामलों, संविदात्मक मुद्दे, आरओयू/आरओडब्ल्यू समस्याएं, कानून और व्यवस्था की स्थिति आदि शामिल हैं ।

7. मंत्रालय के ऑनलाइन कम्प्यूटरीकृत मॉनीटरिंग सिस्टम (ओसीएमएस) में विभिन्न अवसंरचना परियोजनाओं के पीईआरटी चार्टों से तैयार किए गए लक्ष्यों की निगरानी की परिकल्पना की गई है । परियोजना प्राधिकारियों से नियमित रूप से अनुरोध किया गया है कि वे बेहतर निगरानी को सुचारू बनाने के लिए प्रत्येक परियोजना के संबंध में उपलब्धियों की सूची की प्रविष्टि करें । तथापि, सभी परियोजना एजेंसियां उपलब्धियों की

सूची प्रदान नहीं कर रही हैं। पहले शुरू की गई 5 परियोजनाएं जिनके लक्ष्य परियोजना एजेंसियों द्वारा प्रदान नहीं किए जा रहे हैं, नीचे दी गई हैं:-

बिना उपलब्धियों वाली पहली 5 परियोजनाओं की सूची (31.03.2014 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (रु. करोड़)		संचयी व्यय (रु. करोड़)	शुरू करने की तारीख		उपलब्धि
				मूल	अनुमानित		मूल	अनुमानित	
1	हावड़ा-आमता-चंपादंगा एनएल (एससीआर)	रेलवे	04/1974	31.42	535.40	176.52	03/2007	03/2015	एन.आर.
2	नांगल बांध तलवारा (एनएल), एनआर	रेलवे	03/1981	37.68	1036.78	353.41	07/2012	एन.आर.	एन.आर.
3	इकलाखी से बलूरघाट तक नई बी जी रेलवे लाइन	रेलवे	04/1983	36.80	703.17	247.74	एन.आर.	03/2015	एन.आर.
4	फ्रेट आप्रेशनस इन्फोर्मेशन सिस्टम (एफओआईएस)	रेलवे	03/1984	520.00	634.13	555.27	03/1995	03/2013	एन.आर.
5	तामलुक दीघा, लाइन का दोहरीकरण (एसईआर)	रेलवे	03/1984	293.97	1074.47	433.89	06/2005	06/2016	एन.आर.

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार लक्ष्यों को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

एन.आर.: सूचित नहीं।

8. यह पाया गया है कि परियोजना एजेंसियां संशोधित लागत अनुमानों तथा अनेक परियोजनाओं को शुरू करने की समय-सारणी को सूचित नहीं कर रही हैं, जो संकेत देता है कि समय/लागतवृद्धि संबंधी आंकड़े कम

बताए गए हैं । पहले शुरू की गई 5 परियोजनाएं जिनमें परियोजना एजेंसियां संशोधित लागत अनुमानों की सूचना नहीं दे रही हैं/प्रदान नहीं करा रही हैं, नीचे दी गई हैं:-

बिना संशोधित लागत अनुमानों वाली पहली 5 परियोजनाओं की सूची (31.03.2014 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (` करोड़)		संचयी व्यय (` करोड़)
				मूल	संशोधित	
1	लांझीगढ़-जूनागढ़ एनएल (ईसीओआर)	रेलवे	04/1993	100.00	142.98	211.19
2	अमरावती-नरखेर एनएल (सीआर)	रेलवे	06/1994	120.90	284.27	541.95
3	पेड़ापल्ली-करीमनगर-निजामाबाद एनएल (एससीआर)	रेलवे	12/1994	124.43	495.68	597.99
4	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	2500.00	2500.00	8549.43
5	कोट्टूर-हरीहर (एनएल), (एसडब्ल्यूआर)	रेलवे	04/1995	65.94	302.23	344.29

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार संशोधित लागत अनुमानों को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

पहले शुरू की गई 5 परियोजनाएं जिनमें परियोजना एजेंसियां शुरू करने की संशोधित समय-सारणी की सूचना नहीं दे रही हैं/प्रदान नहीं करा रही हैं, नीचे दी गई हैं:-

शुरू करने की संशोधित समय-सारणी के बिना पहली 5 परियोजनाओं की सूची (31.03.2014 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना को शुरू करने की तारीख		
				मूल	संशोधित	अनुमानित
1	नांगल बांध-तलवारा (एनएल), एनआर	रेलवे	03/1981	07/2012	एन.आर.	एन.आर.
2	विरमगाम-भिल्डी (डब्ल्यूआर), जीसी	रेलवे	04/1990	एन.आर.	03/2010	एन.आर.
3	अमरावती-नरखेर एनएल (सीआर)	रेलवे	06/1994	06/1999	03/2011	03/2011
4	पेडापल्ली-करीमनगर-निजामाबाद एनएल (एससीआर)	रेलवे	12/1994	एन.आर.	एन.आर.	03/2012
5	कोटूर-हरीहर (एनएल), (एसडब्ल्यूआर)	रेलवे	04/1995	एन.आर.	एन.आर.	12/2012

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार शुरू करने की संशोधित समय-सारणी को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

एन.आर.: सूचित नहीं ।

9. विलंब/अतिरिक्त विलंब का क्षेत्र-वार ब्यौरा निम्नानुसार है:-

0) नागर विमानन क्षेत्र में 8 परियोजनाओं में से 3 परियोजनाएं विलंबित हैं । 'नए अंतर्राष्ट्रीय टर्मिनल भवन का निर्माण (जीओए) एएआई' नामक परियोजना के संबंध में संरचना संबंधी डिजाइन एवं श्रमिकों की कमी के कारण 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।

00) सड़क क्षेत्र में 132 परियोजनाओं में से 7 परियोजनाएं विलंबित हैं । 'ब्रह्मपुत्र पुल, एनएच सं.-31, एनएचएआई' परियोजना के संबंध में 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

000) **इस्पात क्षेत्र** में 20 परियोजनाओं में से 10 परियोजनाएं विलंबित हैं । परियोजना 'बेलाडिला आइरन ओर परियोजना डिपोजिट-11बी, एनएमडीसी' में आग की दुर्घटना से साउनहिल कन्वेयर को हुए नुकसान के कारण 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।

00) **कोयला क्षेत्र** में 56 परियोजनाओं में से 29 परियोजनाएं विलंबित हैं । 'टीपीएस-00 एक्सपैंशन (1470 मेवा. से 1970 मेवा. तक), एनएलसी' बड़ी परियोजना के संबंध में उपस्करों की आपूर्ति में विलंब तथा ठेकेदार के अपर्याप्त संघटन के कारण 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।

0) **पोत परिवहन तथा पत्तन क्षेत्र** में, 19 परियोजनाओं में से 1 परियोजनाएं विलंबित हैं । परियोजना '2 ऑफशोर कंटेनर बर्थ व टर्मिनल, भारतीय पत्तन निगम के मुम्बई पोर्ट ट्रस्ट (बड़ी परियोजना) का निर्माण और विकास' में 7 माह के अतिरिक्त विलंब की सूचना दी गई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

00) **दूरसंचार क्षेत्र** में, 10 परियोजनाओं में से 4 परियोजनाएं विलंबित हैं । माह के दौरान 3 परियोजनाओं के संबंध में 2-3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । परियोजना 'आपूर्ति स्थापना परीक्षण तथा ग्रामीण वाईमैक्स नेटवर्क की शुरुआत चरण-00, बीएसएनएल' में न्यायालय मामला के कारण 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; तथा परियोजनाएं 'उत्तरांचल में 283000 लाईनों (2जी) तथा 75000 लाईनों (3जी) का जीएसएम उपकरण, बीएसएनएल' और असम दूरसंचार क्षेत्र चरण-0.0, 2जी व 3जी बीएसएनएल' में क्रमशः भूमि अधिग्रहण में विलंब तथा कानून और व्यवस्था की समस्याओं के कारण प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।

000) **रेलवे क्षेत्र** में 282 परियोजनाओं में से 36 परियोजनाएं विलंबित हैं । माह के दौरान, 3 परियोजनाओं के संबंध में 2 से 24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें से 1 बड़ी परियोजना है । परियोजना 'पनवेल पेन डबलिंग, सीआर' के संबंध में परियोजना चालू होने से पहले की शुरुआती समस्याओं के कारण 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'न्यू कूचबिहार-गुमनीहाट पैच डबलिंग परियोजना, एनईएफआर' में निधि की कमी के कारण 24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; तथा परियोजना 'बारानगर से बराकपुर तथा दक्षिणेश्वर (एमटीपी) तक मेट्रो रेल के निर्माण हेतु नया कार्य, आरवीएनएल' में 24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

0000) **विद्युत क्षेत्र** में, 96 परियोजनाओं में से 42 परियोजनाएं विलंबित हैं । माह के दौरान 5 परियोजनाओं के संबंध में 1-5 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें से 3

परियोजनाएं मेगा परियोजनाएं हैं । परियोजनाएं 'बाढ़ एसटीपीपी चरण-00, एनटीपीसी' और 'नॉर्दर्न रिजन ट्रांसमिशन स्ट्रेंथनिंग स्कीम, पीजीसीआईएल' में भेल द्वारा सामग्रियों की आपूर्ति में विलंब तथा आरओयू समस्याओं के कारण प्रत्येक में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'बोंगाइगांव थर्मल पावर परियोजना, एनटीपीसी' में बार-बार बंद के कारण 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'डब्ल्यूआर तथा एनआर हेतु सिस्टम स्ट्रेंथनिंग कॉमन (लाईन बेज तथा रिएक्टर प्रोविजन), पीजीसीआईएल' तथा 'पारवती एच.ई.पी. चरण-000, एनएचपीसी' में क्रमशः 3 तथा 5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है)।

00) **पेट्रोलियम क्षेत्र में,** 76 परियोजनाओं में से 48 परियोजनाएं विलंबित हैं । माह के दौरान 14 परियोजनाओं के संबंध में 2-24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें से 9 परियोजनाएं मेगा परियोजनाएं हैं । परियोजनाएं 'मुम्बई हाई साउथ रिडेवलपमेंट चरण-2, ओएनजीसी', '102 मेगावाट विंड पावर परियोजना, ओएनजीसी' तथा '2000 एचपी ड्रिलिंग आरआईजी के 2 संख्या की खरीद, ऑयल' में क्रमशः कार्य क्षेत्र में परिवर्तन, आरओयू समस्याएं तथा भूमि अधिग्रहण में विलंब के कारण 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'विजयपुर तथा पाटा में पेट्रोकेमिकल कॉम्प्लेक्स-00 गेल' तथा 'सेन्ट्रल गैस गैदरिंग स्टेशन तथा ऑफटेक प्वाइंट, ऑयल' में क्रमशः ठेकेदार के अपर्याप्त संघटन तथा कानून व व्यवस्था की समस्याओं के कारण प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'पॉलीप्रोपीलेन इकाई, मँगलौर रिफाइनरी' तथा 'एमआरपीएल चरण-000 विस्तार, मँगलौर रिफाइनरी' में सिविल तथा संरचनात्मक कार्यों में धीमी प्रगति के कारण 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'डिहाइड्रेशन सुविधा के साथ सेकेंडरी टैंक फार्म का निर्माण तथा मधुबन में ईटीपी, ऑयल' में प्रोजेक्ट साइट को नए लोकेशन में शिफ्ट करने के कारण 5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'मुम्बई रिफाइनरी में डीजल हाइड्रोट्रीटर परियोजना, एचपीसीएल' में चट्टानों की सख्त परतों में बोरिंग में विलंब के कारण 7 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'अहमदाबाद तथा अंकलेश्वर में 6 प्रवाही ट्रीटमेंट प्लांट का निर्माण (ईटीपी), ओएनजीसी' में श्रमिकों की कमी के कारण 15 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'जी1 तथी जीएस-15 का विकास, ओएनजीसी' में लंबी चलने वाली कानूनी कार्रवाईयों की वजहों से 24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'बी-46 कलस्टर क्षेत्रों का विकास, ओएनजीसी' तथा 'मुम्बई हाई नार्थ विकास चरण-00, ओएनजीसी' में प्रत्येक में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; तथा परियोजना 'विशाख रिफाइनरी में डीजल हाइड्रोट्रीटर परियोजना, एचपीसीएल' में 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि,

इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

10. दिनांक 31.03.2014 की स्थिति के अनुसार, विभिन्न क्षेत्रों में ` 150 करोड़ तथा अधिक लागत वाली परियोजनाओं के संबंध में स्थिति रिपोर्ट में सूचित की गई है ।
11. इसे सचिव, सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय का अनुमोदन प्राप्त है ।

EXECUTIVE SUMMARY

1. The Flash Report for March 2014 contains information on the status of the 710 Central Sector Infrastructure Projects costing ₹ 150 crore and above. During March 2014, 14 projects (8 projects are in Petroleum, 5 projects are in Power and 1 project is in Railway Sector) have reported completion.

2. During the reference month, out of 710 projects, 185 projects are delayed with respect to latest schedule and 30 projects have reported additional delays vis-à-vis the date of completion reported in the previous month. Of these 30 projects, 15 are Mega Projects costing ₹ 1000 crore and above.

S. No.	Sector	Projects on monitor	Delayed Projects w.r.t latest schedule	Additionally delayed during the month under report	Additionally delayed Mega Projects
1.	RAILWAYS	282	36	3	1
2.	ROAD TRANSPORT AND HIGHWAYS	132	7	1	0
3.	POWER	96	42	5	3
4.	PETROLEUM	76	48	14	9
5.	COAL	56	29	1	1
6.	STEEL	20	10	1	0
7.	SHIPPING AND PORTS	19	1	1	1
8.	TELECOMMUNICATIONS	10	4	3	0
9.	CIVIL AVIATION	8	3	1	0
10.	URBAN DEVELOPMENT	5	1	0	0
11.	ATOMIC ENERGY	4	4	0	0
12.	PETROCHEMICALS	1	0	0	0
13.	WATER RESOURCES	1	0	0	0
Total		710	185	30	15

3. Total original cost of implementation of the 710 projects was about ₹ 9,24,307.04 crore and their anticipated completion cost is likely to be ₹ 11,03,914.08 crore, which reflects overall cost overruns of ₹ 1,79,607.04 crore (19.40 % of original cost). The expenditure incurred on these projects till March 2014 is ₹ 5,01,798.71 crore, which is 45.50 % of the anticipated cost of the projects. The 5 projects with the maximum percentage cost overruns are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM PERCENTAGE COST OVERRUNS (as on 31-03 -2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹; crore)			COST OVERRUNS (in %)
				ORIGINAL	REVISED	ANTICIPATED	
1	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	37.68	450.00	1036.78	2651.54
2	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	Railways	04/1983	36.80	274.41	703.17	1810.79
3	HOWRAH-AMTA-CHAMPADANGA NL (SER)	Railways	04/1974	31.42	393.46	535.40	1604.01
4	BANKURA - DAMODAR (GC) (SER)	Railways	03/1998	111.90	1028.05	1423.98	1172.55
5	AKOLA-KHANDWA GC AKOLA-AKOT	Railways	04/2008	184.26	N.R.	2000.00	985.42

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

4. The 5 projects with maximum cost overruns in absolute term are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM COST OVERRUNS (as on 31-03-2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹; crore)		
				COST ORIGINAL	COST ANTICIPATED	COST OVERRUN
1	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	2500.00	20000.00	17500.00
2	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	Railways	04/2003	727.56	5996.00	5268.44
3	BANGALORE METRO RAIL PROJECT	Urban Development	05/2006	6395.33	11609.00	5214.00
4	SUBANSIRI LOWER H.E.P (NHPC)	Power	09/2003	6285.33	10667.00	4381.67
5	KUDANKULAM APP (NPCIL)	Atomic Energy	12/2001	13171.00	17270.00	4099.00

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

5. Out of the 710 projects, 3 projects are ahead of schedule, 156 are on schedule and 185 are delayed with respect to latest schedule. However, the numbers of delayed projects further increases to 209 if delay is calculated on the basis of original schedule of completion. Further,

23 projects have been sanctioned without any commissioning schedule/date and for 343 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 185 delayed projects, 40 projects have overall delay in the range of 1 to 12 months, 43 projects have a delay in the range of 13 to 24 months, 63 projects have a delay in the range of 25 to 60 months and 39 projects have a delay of 61 months and above. The 5 projects with the maximum delay are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM TIME OVERRUNS (as on 31-03-2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	DATE OF COMMISSIONING		TIME OVERRUNS (in months)
				ORIGINAL	ANTICIPATED	
1	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	Railways	03/1984	03/1995	03/2015	240
2	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	Railways	04/1986	03/1994	10/2013	238
3	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	04/1993	03/2002	09/2013	143
4	BANKURA - DAMODAR (GC) (SER)	Railways	03/1998	03/2005	12/2016	141
5	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	03/2001	12/2017	181

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further time overruns.

6. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, forest clearance, delay in supply of equipments, fund constraints, geological surprises, equipment erection, geo-mining condition, shortage of labour, inadequate mobilization by the contractor, court cases, contractual issue, ROU/ROW problems, law and order situation, etc.

7. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones drawn from the PERT Charts of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The earliest initiated 5 projects in which project agencies are not providing milestones are as below:-

List of 5 Earliest Projects without Milestones (as on 31-03-2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹; crore)		EXPENDITURE CUMMULATIVE (₹; crore)	DATE OF COMMISSIONING		MILE STONES
				ORIGINAL	ANTICIPATED		ORIGINAL	ANTICIPATED	
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	Railways	04/1974	31.42	535.40	176.52	03/2007	03/2015	N.R.
2	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	37.68	1036.78	353.41	07/2012	N.R.	N.R.
3	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT	Railways	04/1983	36.80	703.17	247.74	N.R.	03/2015	N.R.
4	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	Railways	03/1984	520.00	634.13	555.27	03/1995	03/2013	N.R.
5	TAMLUK DIGHA,LINE DOUBLING (SER)	Railways	03/1984	293.97	1074.47	433.89	06/2005	06/2016	N.R.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up milestones.

N.R.: Not Reported.

8. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The earliest initiated 5 projects in which project agencies are not reporting/providing revised cost estimates are as below:-

List of 5 Earliest Projects without Revised Cost Estimates (as on 31-03-2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹; crore)		EXPENDITURE CUMMULATIVE (₹; crore)
				ORIGINAL	REVISED	
1	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	04/1993	100.00	142.98	211.19
2	AMRAVATI-NARKHER NL(CR)	Railways	06/1994	120.90	284.27	541.95
3	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	12/1994	124.43	495.68	597.99
4	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	2500.00	2500.00	8549.43
5	KOTTUR-HARIHAR(NL),(SWR)	Railways	04/1995	65.94	302.23	344.29

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised cost estimates.

The earliest initiated 5 projects in which project agencies are not reporting/providing revised commissioning schedules are as below:-

List of 5 Earliest Projects without Revised Commissioning Schedule (as on 31.03.2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	DATE OF COMMISSIONING		
				ORIGINAL	REVISED	ANTICIPATED
1	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	07/2012	N.R.	N.R.
2	VIRAMGAM-BHILDI(WR),GC	Railways	04/1990	N.R.	03/2010	N.R.
3	AMRAVATI-NARKHER NL(CR)	Railways	06/1994	06/1999	03/2011	03/2011
4	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	12/1994	N.R.	N.R.	03/2012
5	KOTTUR-HARIHAR(NL),(SWR)	Railways	04/1995	N.R.	N.R.	12/2012

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised commissioning schedule.

N.R.: Not Reported.

9. **The Sector-wise details of delays/additional delays are as under:-**

i) In the **Civil Aviation Sector**, out of 8 projects, 3 projects are delayed. The project 'Construction of New International Terminal Building (GOA), AAI' has reported additional delay of 1 month due to change in structural design and shortage of labour.

ii) In the **Road Sector**, out of 132 projects, 7 projects are delayed. The project 'Brahmaputra Bridge, NH No-31, NHAI' has reported additional delay of 4 months (however, no specific reasons have been reported by the project authority for the delay in this project).

iii) In the **Steel Sector**, out of 20 projects, 10 projects are delayed. The project 'Bailadila Iron Ore Project Deposit- 11B, NMDC' has reported additional delay of 4 months due to a fire accident that damaged sown hill conveyor.

iv) In the **Coal Sector**, out of 56 projects, 29 projects are delayed. The project 'TPS-II Expansion (1470MW to 1970MW), NLC' (Mega Project) has reported additional delay of 1 month due to delay in equipment erection and inadequate mobilization by the contractor.

v) In the **Shipping & Ports Sector**, out of 19 projects, 1 project is delayed. The project 'Construction & Development of 2 Offshore Container Berths & Terminal, Mumbai Port Trust of Shipping Corporation of India' (Mega project) has reported additional delay of 7 months (however, no specific reasons have been reported by the project authority for the delay in this project).

vi) In the **Telecommunication Sector**, out of 10 projects, 4 projects are delayed. During the month 3 projects have reported additional delays in the range of 2-3 months. The project 'Supply Installation Testing and Commissioning of Rural Wimax Network Phase-II, BSNL' has reported additional delay of 2 months due to court case; and the projects 'GSM Equipment of 283000 Lines (2G) And 75000 Lines (3G) in Uttranchal, BSNL' and 'Assam Telecom Circle, Phase-V.I, 2G & 3G, BSNL' have reported additional delays of 3 months each due to delay in land acquisition and law & order problems respectively.

vii) In the **Railways Sector**, out of 282 projects, 36 projects are delayed. During the month 3 projects have reported additional delays in the range of 2-24 months, out of which 1 is Mega project. The project 'Panvel Pen Doubling, CR' has reported additional delay of

2 months due to pre-commissioning teething problem; the project 'New Coochbehar-Gumanihat Patch Doubling Project, NEFR' has reported additional delay of 24 months due to fund constraints; and the project 'New Work for Construction of Metro Railway from Baranagar to Barrackpore and Dakshineswar (MTP), RVNL' has reported additional delay of 24 months (however, no specific reasons have been reported by the project authority for the delay in this project).

viii) In the **Power Sector**, out of 96 projects, 42 projects are delayed. During the month 5 projects have reported additional delays in the range of 1-5 months, out of which 3 are Mega projects. The projects 'Barh STPP Stage –II, NTPC' and 'Northern Region Transmission Strengthening Scheme, PGCIL' have reported additional delay of 1 month each due to delay in supply of materials by BHEL and ROW problems; the project 'Bongaigaon Thermal Power Project, NTPC' has reported additional delay of 2 months due to frequent bandhs ; and the projects 'System Strengthening Common For WR and NR (Line Bays and Reactor Provision), PGCIL' and 'Parbati H.E.P. Stage –III, NHPC' have reported additional delays of 3 and 5 months respectively (however, no specific reason has been reported by the project authorities for the delay in these projects).

ix) In the **Petroleum Sector**, out of 76 projects, 48 projects are delayed. During the month 14 projects have reported additional delays in the range of 2-24 months, out of which 9 are Mega projects. The projects 'Mumbai High South Redevelopment Ph-2, ONGC' , '102 MW Wind Power Project, ONGC' and 'Purchase of 2 Nos. of 2000 HP Drilling RIG, OIL' have reported additional delays of 2 months each due to change of scope of works, ROW problems and delay in land acquisition respectively; the projects 'Petrochemical Complex-II at Vijaypur and Pata, GAIL' and 'Central Gas Gathering Station and Offtake Point, OIL' have reported additional delays of 3 months each due inadequate mobilization by the contractor and law & order problems respectively; the projects 'Polypropylene Unit, Mangalore Refinery' and 'MRPL Phase-III Expansion, Mangalore Refinery' have reported additional delays of 3 months each due to slow progress in civil and structural works; the project 'Creation of Secondary Tank Farm with Dehydration Facility and ETP at Madhuban, OIL' has reported additional delay of 5 months due to shifting of project site to new location; the project 'Diesel Hydrotreater Project at Mumbai Refinery, HPCL' has reported additional delay of 7 months due to delay in boring on hard rock strata; the project 'Construction of Six Effluent Treatment Plants (ETP), Ahmedabad and Ankleswar, ONGC' has reported additional delay of 15 months due to shortage of labour; the project 'Development of G1 and GS-15, ONGC' has reported additional delay of 24 months due to prolonged legal proceedings; the projects

‘Development of B-46 Cluster Field, ONGC’ and ‘Mumbai High North Development Phase-II, ONGC’ have reported additional delays of 2 months each; and the project ‘Diesel Hydrotreater Project at Visakh Refinery, HPCL’ has reported additional delay of 4 months (however, no specific reasons have been reported by the project authorities for the delay in these projects).


10. The status as on 31.03.2014 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

11. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

EXECUTIVE SUMMARY

Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	282	3
2	ROAD TRANSPORT AND HIGHWAYS	132	1
3	POWER	96	5
4	PETROLEUM	76	14
5	COAL	56	1
6	STEEL	20	1
7	SHIPPING AND PORTS	19	1
8	TELECOMMUNICATIONS	10	3
9	CIVIL AVIATION	8	1
10	URBAN DEVELOPMENT	5	0
11	ATOMIC ENERGY	4	0
12	PETROCHEMICALS	1	0
13	WATER RESOURCES	1	0
	Total	710	30

Sectoral break up of on-going infrastructure projects.

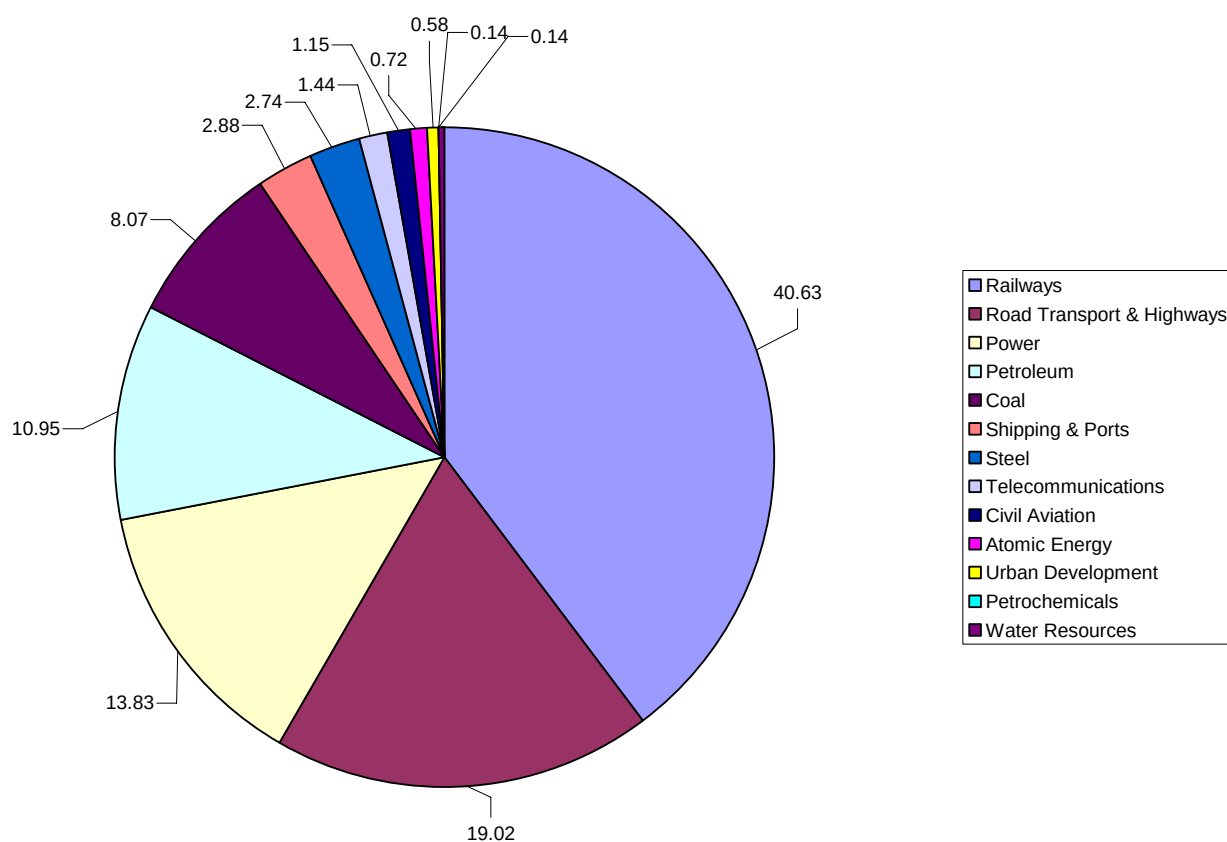

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2013-2014				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2013			
	<u>POWER</u>			
1	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000091]	209.78	08/2013	52.2
	<u>RAILWAYS</u>			
2	RENIGUNTA-GUNTAKAL(RE) (RAIL VIKAS NIGAM LTD.) - [220100260]	168.34	04/2003	343.36
3	BILASPUR-URKURA (DL) (RAIL VIKAS NIGAM LTD.) - [220100321]	151.52	-	315
	May,2013			
	<u>FERTILISERS</u>			
4	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT (NATIONAL FERTILISER LIMITED) - [N08000006]	1,478.63	01/2013	1133
	<u>POWER</u>			
5	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PART-I (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000068]	1,347.32	02/2012	1206.1
6	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION GRID - PART-II (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000078]	1,736.36	06/2012	1240.75
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
7	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106250]	340.68	03/2008	400.56
	June,2013			
	<u>RAILWAYS</u>			
8	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) (RAIL VIKAS NIGAM LTD.) - [N22000027]	240.00	03/2009	334.59
9	PANSPURA-KHARAGPUR 3D LINE (RAIL VIKAS NIGAM LTD.) - [N22000076]	252.50	02/2010	249.36
	July,2013			
	<u>PETROLEUM</u>			
10	NORTH TAPTI GAS FIELD DEVELOPMENT (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000096]	589.70	03/2011	912.53

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2013-2014				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	<u>POWER</u>			
11	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC) (NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [180100222]	768.92	03/2007	1467.53
12	CHUTAK HYDRO-ELECTRIC PROJECT (NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [N18000007]	621.26	02/2011	731.93
	August,2013			
13	INTERCONNECTION BETWEEN ELECTTRICAL GRIDS OF INDIA AND BANGLADESH -INDIAN PORTION (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000089]	160.32	10/2012	87.63
	<u>RAILWAYS</u>			
14	MADURAI-RAMESWARAM-GC (SOUTHERN RAILWAY) - [N22000200]	240.00	-	367.21
15	KRISHNANAGAR-BETHUA DAHRI DOUBLING (EASTERN RAILWAYS) - [N22000226]	151.65	03/2015	90.21
16	DHARMAVARAM-PAKALA GC (SAUTH COST RAILWAY) - [N22000284]	294.99	-	658.53
	September,2013			
	<u>PETROLEUM</u>			
17	BUTADIENE EXTRACTION UNIT(BDEU) AT PANIPAT (INDIAN OIL CORPORATION LIMITED) - [N16000108]	341.50	02/2013	198.81
	<u>POWER</u>			
18	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA MEGA POWER PROJECT (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000046]	7,031.88	12/2012	4591.9
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
19	GWALIOR BYPASS, NH-75,3 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000088]	300.93	10/2009	302.7
	October,2013			
	<u>POWER</u>			
20	NIMOO BAZGO HYDROELECTRIC PROJECT (NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [N18000006]	611.01	08/2010	883.85
21	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000018]	557.24	01/2010	648.43
	<u>RAILWAYS</u>			
22	CHANDIGARH-LUDHIANA(NEW BG LINE),NR (NORTHERN RAILWAY) - [220100241]	248.44	12/2012	972.91

Month wise List of Completed Projects Costing Rs. 150 crore and above during 2013-2014				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
23	RUPSA-BANGRIPOSI (GC)(SER) (SOUTH EASTERN RAILWAY) - [220100323]	57.94	03/1998	176.14
	<u>TELECOMMUNICATIONS</u>			
24	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 9920/05-06 (MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000029]	231.38	10/2007	86.11
	November,2013			
	<u>RAILWAYS</u>			
25	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) (SOUTH WESTERN RAILWAY) - [220100190]	157.00	03/2012	330.38
	December,2013			
	<u>PETROLEUM</u>			
26	RESITMENT OF MARKETING INSTALATION AT VISAKH (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000057]	756.00	-	913.72
27	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000066]	224.00	-	312.61
28	FLUIDIZED CATALYTIC CRACKING UNIT(FCCU) REVAMP AT MATHURA REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000107]	1,000.00	01/2013	755.25
29	CAPACITY AUGMENTATION OF KOTA PIYALA SECTION OF MMBPL PIPELINE (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000153]	152.89	06/2013	128.53
	<u>RAILWAYS</u>			
30	KOLAR-CHICKBALAPUR GC (SOUTH WESTERN RAILWAY) - [N22000275]	287.99	01/1999	434.57
	January,2014			
	<u>PETROLEUM</u>			
31	ADDITIONAL GAS PROCESSING UNITS AT URAN (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000064]	1,797.35	12/2011	841.98
	<u>POWER</u>			
32	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION GRID - PART-III (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000079]	1,075.12	05/2012	N.A.
33	ESTABLISHMENT OF POOLING STATIONS AT RAJGARH AND RAIPUR FOR IPP GENERATION PROJECTS IN CHATTISGARH (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000092]	1,719.52	08/2013	N.A.
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2013-2014				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
34	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240101132]	241.00	08/2004	67.03
35	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240101133]	318.00	08/2004	71.35
36	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240101153]	225.00	04/2004	109.99
37	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106205]	220.00	09/2007	282.7
38	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106237]	284.00	05/2008	350.7
39	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106243]	240.00	10/2008	295.51
40	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106260]	190.00	01/2009	264.65
41	NEW MANGALORE PORT NH-17 AND 48 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000040]	196.50	06/2011	290.98
42	NAGPUR-KONDHALI,NH-6(NHAI) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000055]	168.00	12/2008	457.3
43	THANJAUR-TRICHY,NH-67(NHAI) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000056]	280.00	06/2009	581.5
44	GANJAM-ICCHAPURUM,NH-5(NHAI) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000057]	263.27	02/2004	263.96
45	LAKHNAADON TO MP/MH BORDER,KM 596.75-653.22 (NS-1/BOT/MP-2),NH7 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000094]	407.60	06/2010	186.77
46	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000095]	263.17	09/2009	235.19
47	JHANSI TO LALITPUR, NH-25,26 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000096]	355.06	09/2009	507.99
48	TRICHY - KORUR NH-67 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000101]	516.00	07/2010	866.86
49	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000102]	941.00	01/2011	1901
50	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000116]	228.70	02/2004	182.07
51	FOUR LANNING FROM MP/MAHARASHTRA BORDER TO NAGPUR, NAGPUR BYPASS (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000124]	1,170.52	06/2011	4.41
52	GURGAON-KOTPUTLI KM 42.70 TO 54.4 KM (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000130]	1,673.70	10/2011	2866.54
53	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000131]	1,693.75	08/2011	2760.82
	February,2014			
	<u>POWER</u>			
54	URI H.E.P STAGE -II (NHPC) (NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [180100251]	1,729.29	11/2009	2104.1
	<u>RAILWAYS</u>			
55	KOTTUR-HARIHAR(NL),(SWR) (SOUTH WESTERN RAILWAY) - [220100212]	65.94	-	366.03

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2013-2014				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	March,2014			
	<u>PETROLEUM</u>			
56	IOR LAKWA - LAKHMANI (ONGCL) (OIL & NATURAL GAS CORPORATION LIMITED) - [160100215]	345.10	03/2007	743.72
57	IOR GELEKI (ONGCL) (OIL & NATURAL GAS CORPORATION LIMITED) - [160100216]	390.09	03/2007	1759.52
58	IOR, RUDRASAGAR (ONGCL) (OIL & NATURAL GAS CORPORATION LIMITED) - [160100217]	113.90	03/2006	452.91
59	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000031]	740.02	03/2010	739.83
60	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000081]	825.00	04/2013	1545
61	DEVELOPMENT OF SB-14 FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000116]	410.44	11/2012	337.16
62	DEVELOPMENT OF BHE AND BH-35 AREA. (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000118]	372.11	03/2013	334.31
63	BUTENE-1 PROJECT AT PANIPAT (INDIAN OIL CORPORATION LIMITED) - [N16000139]	190.00	03/2014	125.28
	<u>POWER</u>			
64	EASTERN REGION STRENGTHENING SCHEME-I (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000004]	975.96	10/2009	N.A.
65	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000052]	520.48	11/2011	N.A.
66	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000088]	182.68	01/2013	N.A.
67	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VELLUR TPS (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000097]	170.36	04/2013	N.A.
68	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUB STATION AT KALA IN UT DNH (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000102]	181.93	07/2013	N.A.
	<u>RAILWAYS</u>			
69	LANJHIGARH-JUNAGARH NL(ECOR) (EAST COAST RAILWAY) - [220100148]	100.00	03/2002	243.27


Summary of projects in the Flash Report for the month of March, 2014

Project Implementation - Current Status:

Number of Projects in Previous Month	721
Number of Projects completed/dropped/frozen in Current Month	14
Number of Projects elevated to the status of Major project during the current month	1
Number of Projects Added in Current Month	2
Number of Projects in Current Month	710


Brief Analysis

Project Status with respect to Original Schedule: Out of 710 projects, 3 projects are ahead of schedule, 132 projects are on schedule and 209 projects are delayed. Of the balance, 343 projects do not have fixed dates of commissioning while 23 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

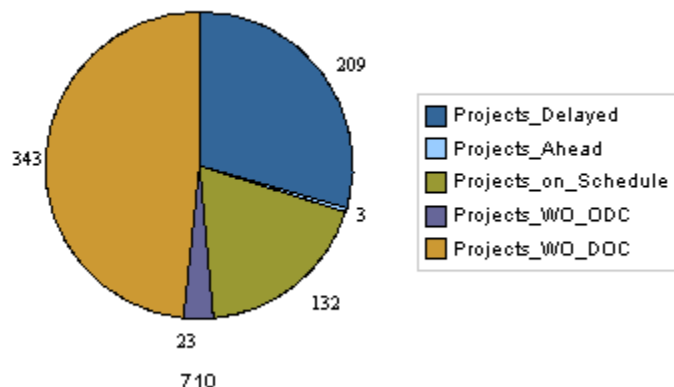

Investment Scenario

The Total Original cost of implementation of 710 projects when sanctioned, was of the order of Rs. 924307.04 crore but this was subsequently revised to Rs. 1103914.08 crore implying a cost overrun of 19.4%. The expenditure incurred on these projects till March, 2014 is Rs. 501798.71 crore, which is 45.5% of the revised cost of the projects.

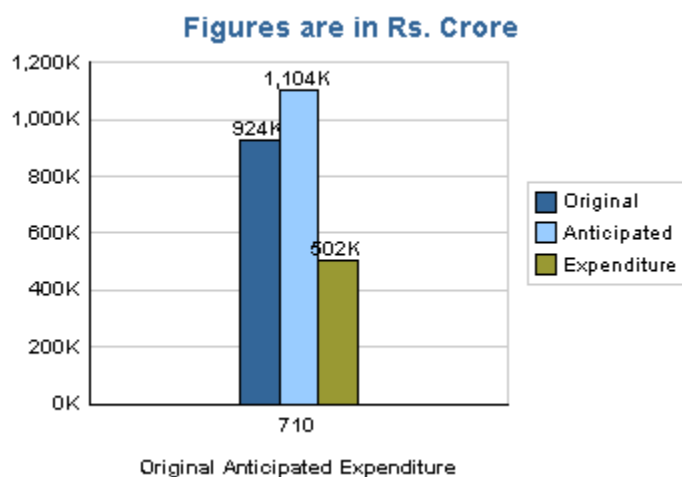

Projects Added / Completed / Dropped / Frozen

No of Projects in Previous Month	721
No of Projects Completed/Dropped/Frozen in Current Month	14
No of Projects elevated to status of Major Project during the current months	1
No of Projects added in Current Month	2
No of Projects in Current Month	710

Project status							
Number of Projects							
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total	Delayed Projects (%)
Original (Date)	209	3	132	23	343	710	29.44
Latest Approved (Date)	185	3	156	23	343	710	26.06

Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	561	8,04,015.45	8,64,832.22	3,60,058.52	41.60	60,816.77	7.60
Project with Revision in Cost	149	1,86,867.12	2,39,081.86	1,41,740.19	59.30	52,214.74	27.90
Total	710	9,90,882.57	11,03,914.08	5,01,798.71	45.46	113031.51	11.41
Original Cost of All Projects							
Original Cost	710	9,24,307.04	11,03,914.08	5,01,798.71	45.50	1,79,607.04	19.40

Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	209	437,808.63	538,749.72	306,414.63	56.90	100,941.09	23.10
Latest Approved (RCE)	185	453,849.21	512,494.67	296,343.81	57.80	58,645.46	12.90

Additional Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	30	69,793.91	75,396.75	59,201.28	78.50	5,602.84	8.00

Extent of cost overrun in projects with respect to original schedule(Sector Wise)									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	40,442.0	46,726.0	15.5	2	16,663.0	22,947.0	37.7
2	CIVIL AVIATION	8	6,035.5	6,946.0	15.1	3	4,086.1	4,996.7	22.3
3	COAL	56	38,737.4	48,559.5	25.4	8	9,767.8	20,187.6	106.7
4	STEEL	20	65,959.3	72,188.6	9.4	8	24,551.0	30,810.3	25.5
5	PETROCHEMICALS	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	63.4
6	PETROLEUM	76	182,981.1	197,259.2	7.8	20	58,401.4	76,352.5	30.7
7	POWER	96	244,469.9	263,493.1	7.8	17	49,844.6	68,867.8	38.2
8	RAILWAYS	282	148,551.6	257,231.7	73.2	145	62,948.7	171,741.0	172.8
9	ROAD TRANSPORT AND HIGHWAYS	132	96,437.2	98,553.2	2.2	13	3,680.5	5,821.2	58.2
10	SHIPPING AND PORTS	19	15,617.1	18,600.6	19.1	9	8,629.0	11,916.7	38.1
11	TELECOMMUNICATIONS	10	5,079.3	4,982.9	-1.9	3	1,394.0	1,481.5	6.3
12	URBAN DEVELOPMENT	5	73,993.3	79,266.2	7.1	2	6,509.2	11,782.1	81.0
13	WATER RESOURCES	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		710	924,307.0	1,103,914.1	19.4	232	252,478.7	437,011.4	73.1

Extent of cost overrun in projects with respect to original schedule(State Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overrun			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	47	37,177.3	45,353.9	22.0	14	12,772.4	21,816.0	70.8
2	ARUNACHAL PRADESH	4	9,512.2	16,855.7	77.2	4	9,512.2	16,855.7	77.2
3	ASSAM	37	23,180.2	34,385.2	48.3	15	11,228.5	22,529.4	100.6
4	BIHAR	45	32,339.0	40,462.9	25.1	17	13,347.2	21,487.4	61.0
5	GOA	1	335.6	388.5	15.8	1	335.6	388.5	15.8
6	GUJARAT	33	38,022.7	39,136.7	2.9	7	3,021.0	4,413.4	46.1
7	HARYANA	8	4,209.9	6,407.6	52.2	3	1,585.8	3,783.5	138.6
8	HIMACHAL PRADESH	5	13,845.2	20,316.0	46.7	4	11,798.2	18,269.0	54.8
9	JAMMU AND KASHMIR	7	11,965.4	30,895.6	158.2	3	4,904.9	23,835.1	385.9
10	KARNATAKA	34	79,459.7	91,331.4	14.9	13	11,585.5	23,795.5	105.4
11	KERALA	12	22,610.7	25,135.4	11.2	5	5,480.4	8,005.2	46.1
12	MADHYA PRADESH	19	30,777.4	32,003.8	4.0	5	3,317.9	4,963.7	49.6
13	MAHARASHTRA	51	93,259.9	108,834.4	16.7	19	34,123.5	50,903.8	49.2
14	MANIPUR	1	727.6	4,478.2	515.5	1	727.6	4,478.2	515.5
15	MEGHALAYA	3	4,845.0	4,845.0	0.0	0	0.0	0.0	0.0
16	MIZORAM	2	1,533.0	3,307.1	115.7	1	619.3	2,393.5	286.5
17	NAGALAND	2	5,124.0	5,124.0	0.0	0	0.0	0.0	0.0
18	ODISHA	28	55,789.0	62,373.1	11.8	11	32,675.6	39,259.7	20.1
19	PUNJAB	4	1,680.2	1,680.2	0.0	0	0.0	0.0	0.0
20	RAJASTHAN	25	25,380.5	25,805.9	1.7	6	2,489.1	3,400.6	36.6
21	SIKKIM	2	1,648.9	3,690.0	123.8	1	1,339.5	3,380.6	152.4
22	TAMIL NADU	38	51,742.7	67,974.4	31.4	20	30,997.2	47,228.9	52.4
23	TRIPURA	6	2,966.3	3,987.7	34.4	3	2,129.4	3,185.2	49.6
24	UTTAR PRADESH	28	21,357.8	25,954.0	21.5	11	4,111.1	8,755.6	113.0
25	WEST BENGAL	36	49,851.1	61,349.5	23.1	17	23,207.4	34,705.8	49.5
26	CHANDIGARH	1	452.0	452.0	0.0	0	0.0	0.0	0.0
27	DELHI	4	41,533.9	41,531.3	-0.0	0	0.0	0.0	0.0
28	CHHATISGARH	23	56,979.1	64,487.8	13.2	6	2,585.1	10,093.7	290.5
29	JHARKHAND	27	16,118.8	20,383.6	26.5	8	2,534.9	6,971.4	175.0
30	UTTARAKHAND	6	7,844.0	10,085.1	28.6	4	5,839.0	8,080.1	38.4
31	MULTI STATE	171	182,037.7	204,897.8	12.6	33	20,210.4	44,032.1	117.9
Total		710	924,307.0	1,103,914.1	19.4	232	252,478.7	437,011.4	73.1

Extent of time overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.0	46,726.0	15.5	4	40,442.0	46,726.0	3 - 72
2	CIVIL AVIATION	8	6,035.5	6,946.0	15.1	3	989.4	1,042.3	7 - 50
3	COAL	56	38,737.4	48,559.5	25.4	30	26,241.1	36,434.6	12 - 120
4	STEEL	20	65,959.3	72,188.6	9.4	13	64,208.3	70,162.3	10 - 67
5	PETROCHEMICALS	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
6	PETROLEUM	76	182,981.1	197,259.2	7.8	50	139,493.4	153,758.7	3 - 122
7	POWER	96	244,469.9	263,493.1	7.8	44	124,490.4	142,171.6	1 - 113
8	RAILWAYS	282	148,551.6	257,231.7	73.2	37	28,589.3	73,021.5	3 - 240
9	ROAD TRANSPORT AND HIGHWAYS	132	96,437.2	98,553.2	2.2	19	5,986.2	6,830.1	5 - 82
10	SHIPPING AND PORTS	19	15,617.1	18,600.6	19.1	4	2,856.3	4,264.9	2 - 99
11	TELECOMMUNICATIONS	10	5,079.3	4,982.9	-1.9	4	2,018.2	1,843.9	36 - 65
12	URBAN DEVELOPMENT	5	73,993.3	79,266.2	7.1	1	2,494.0	2,494.0	8 - 8
13	WATER RESOURCES	1	542.9	1,187.0	118.6	0	0.0	0.0	-
Total		710	924,307.0	1,103,914.1	19.4	209	437,808.6	538,749.7	

Extent of time overrun in projects with respect to original schedule(State Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	47	37,177.3	45,353.9	22.0	9	14,967.8	19,374.4	24 - 67
2	ARUNACHAL PRADESH	4	9,512.2	16,855.7	77.2	3	9,356.2	16,449.3	25 - 94
3	ASSAM	37	23,180.2	34,385.2	48.3	24	14,062.2	20,978.5	3 - 116
4	BIHAR	45	32,339.0	40,462.9	25.1	5	17,679.5	22,043.6	19 - 98
5	GOA	1	335.6	388.5	15.8	1	335.6	388.5	23 - 23
6	GUJARAT	33	38,022.7	39,136.7	2.9	9	20,938.6	20,960.2	4 - 27
7	HARYANA	8	4,209.9	6,407.6	52.2	2	767.1	767.1	46 - 50
8	HIMACHAL PRADESH	5	13,845.2	20,316.0	46.7	3	10,751.3	15,302.0	46 - 106
9	JAMMU AND KASHMIR	7	11,965.4	30,895.6	158.2	2	4,738.7	23,642.0	10 - 181
10	KARNATAKA	34	79,459.7	91,331.4	14.9	7	17,259.3	17,503.3	10 - 44
11	KERALA	12	22,610.7	25,135.4	11.2	3	15,900.0	16,600.0	5 - 41
12	MADHYA PRADESH	19	30,777.4	32,003.8	4.0	3	1,160.4	1,273.2	3 - 69
13	MAHARASHTRA	51	93,259.9	108,834.4	16.7	19	40,526.5	49,329.6	2 - 129
14	MANIPUR	1	727.6	4,478.2	515.5	1	727.6	4,478.2	72 - 72
15	MEGHALAYA	3	4,845.0	4,845.0	0.0	0	0.0	0.0	-
16	MIZORAM	2	1,533.0	3,307.1	115.7	2	1,533.0	3,307.1	35 - 113
17	NAGALAND	2	5,124.0	5,124.0	0.0	1	850.0	850.0	24 - 24
18	ODISHA	28	55,789.0	62,373.1	11.8	13	48,730.8	51,955.7	3 - 84
19	PUNJAB	4	1,680.2	1,680.2	0.0	0	0.0	0.0	-
20	RAJASTHAN	25	25,380.5	25,805.9	1.7	2	13,426.0	12,998.0	3 - 25
21	SIKKIM	2	1,648.9	3,690.0	123.8	2	1,648.9	3,690.0	15 - 50
22	TAMIL NADU	38	51,742.7	67,974.4	31.4	8	32,091.3	41,520.3	3 - 99
23	TRIPURA	6	2,966.3	3,987.7	34.4	4	2,417.4	3,438.9	16 - 120
24	UTTAR PRADESH	28	21,357.8	25,954.0	21.5	7	4,312.0	6,902.6	10 - 84
25	WEST BENGAL	36	49,851.1	61,349.5	23.1	12	28,559.0	33,495.0	3 - 141
26	CHANDIGARH	1	452.0	452.0	0.0	0	0.0	0.0	-
27	DELHI	4	41,533.9	41,531.3	-0.0	1	2,494.0	2,494.0	8 - 8
28	CHHATISGARH	23	56,979.1	64,487.8	13.2	11	35,799.6	42,535.0	6 - 120
29	JHARKHAND	27	16,118.8	20,383.6	26.5	11	9,178.6	9,762.2	16 - 126
30	UTTARAKHAND	6	7,844.0	10,085.1	28.6	4	6,097.2	8,228.1	5 - 60
31	MULTI STATE	171	182,037.7	204,897.8	12.6	40	81,500.2	88,483.0	1 - 240
Total		710	924,307.0	1,103,914.1	19.4	209	437,808.6	538,749.7	

Extent of time overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.0	46,726.0	15.5	4	40,442.0	46,726.0	3 - 72
2	CIVIL AVIATION	8	6,035.5	6,946.0	15.1	3	989.4	1,042.3	7 - 50
3	COAL	56	38,737.4	48,559.5	25.4	29	25,052.8	28,822.2	12 - 84
4	STEEL	20	65,959.3	72,188.6	9.4	10	62,441.9	68,084.6	10 - 67
5	PETROCHEMICALS	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
6	PETROLEUM	76	182,981.1	197,259.2	7.8	48	135,390.6	146,257.9	3 - 122
7	POWER	96	244,469.9	263,493.1	7.8	42	123,002.8	140,129.6	1 - 106
8	RAILWAYS	282	148,551.6	257,231.7	73.2	36	28,264.3	71,905.0	3 - 240
9	ROAD TRANSPORT AND HIGHWAYS	132	96,437.2	98,553.2	2.2	7	2,693.0	3,031.1	5 - 80
10	SHIPPING AND PORTS	19	15,617.1	18,600.6	19.1	1	1,228.0	2,158.2	58 - 58
11	TELECOMMUNICATIONS	10	5,079.3	4,982.9	-1.9	4	2,018.2	1,843.9	36 - 65
12	URBAN DEVELOPMENT	5	73,993.3	79,266.2	7.1	1	2,494.0	2,494.0	8 - 8
13	WATER RESOURCES	1	542.9	1,187.0	118.6	0	0.0	0.0	-
Total		710	924,307.0	1,103,914.1	19.4	185	424,016.9	512,494.7	

Extent of cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overruns			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	40,442.0	46,726.0	15.5	2	16,663.0	22,947.0	37.7
2	CIVIL AVIATION	8	6,625.0	6,946.0	4.8	2	2,660.6	2,981.7	12.1
3	COAL	56	48,533.9	48,559.5	0.1	4	1,431.8	1,716.6	19.9
4	STEEL	20	70,209.4	72,188.6	2.8	3	14,993.1	17,002.3	13.4
5	PETROCHEMICALS	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	63.4
6	PETROLEUM	76	194,954.0	197,259.2	1.2	8	37,444.4	41,445.6	10.7
7	POWER	96	250,470.2	263,493.1	5.2	13	39,844.9	52,867.9	32.7
8	RAILWAYS	282	179,685.2	257,231.7	43.2	114	63,052.0	140,670.8	123.1
9	ROAD TRANSPORT AND HIGHWAYS	132	97,339.9	98,553.2	1.2	5	1,969.8	3,229.7	64.0
10	SHIPPING AND PORTS	19	17,488.0	18,600.6	6.4	6	4,617.6	5,941.7	28.7
11	TELECOMMUNICATIONS	10	5,079.3	4,982.9	-1.9	3	1,394.0	1,481.5	6.3
12	URBAN DEVELOPMENT	5	74,052.2	79,266.2	7.0	1	6,395.0	11,609.0	81.5
13	WATER RESOURCES	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		710	990,882.6	1,103,914.1	11.4	163	196,469.7	312,000.6	58.8

Extent of time & cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	0	0.00	0.00	0- 0
2	CIVIL AVIATION	8	6,035.46	6,946.00	15.09	1	1,808.00	2,015.00	13- 13
3	COAL	56	38,737.38	48,559.52	25.36	1	1,188.31	7,612.33	120- 120
4	STEEL	20	65,959.26	72,188.55	9.44	5	9,557.89	13,808.07	37- 67
5	PETROCHEMICALS	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
6	PETROLEUM	76	182,981.12	197,259.22	7.80	7	19,587.43	31,889.59	20- 122
7	POWER	96	244,469.88	263,493.12	7.78	1	1,657.00	2,978.86	79- 79
8	RAILWAYS	282	148,551.55	257,231.72	73.16	14	5,512.51	21,838.23	0- 141
9	ROAD TRANSPORT AND HIGHWAYS	132	96,437.15	98,553.21	2.19	7	1,496.26	2,039.07	0- 81
10	SHIPPING AND PORTS	19	15,617.12	18,600.58	19.10	5	5,400.70	7,558.41	10- 99
11	TELECOMMUNICATIONS	10	5,079.29	4,982.94	-1.90	0	0.00	0.00	0- 0
12	URBAN DEVELOPMENT	5	73,993.32	79,266.22	7.13	0	0.00	0.00	0- 0
13	WATER RESOURCES	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		710	924307.04	1103914.08	19.43	41	46208.1	89739.56	

Extent of time & cost overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	2	16,663.00	22,947.00	54- 72
2	CIVIL AVIATION	8	6,035.46	6,946.00	15.09	1	335.61	388.53	23- 23
3	COAL	56	38,737.38	48,559.52	25.36	6	9,127.17	19,498.95	24- 120
4	STEEL	20	65,959.26	72,188.55	9.44	4	23,538.89	29,522.85	30- 67
5	PETROCHEMICALS	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
6	PETROLEUM	76	182,981.12	197,259.22	7.80	17	55,437.09	72,673.84	3- 122
7	POWER	96	244,469.88	263,493.12	7.78	14	42,009.56	59,690.70	10- 106
8	RAILWAYS	282	148,551.55	257,231.72	73.16	31	22,111.99	66,553.74	9- 240
9	ROAD TRANSPORT AND HIGHWAYS	132	96,437.15	98,553.21	2.19	8	1,628.10	2,471.98	57- 80
10	SHIPPING AND PORTS	19	15,617.12	18,600.58	19.10	3	2,344.46	3,752.98	2- 99
11	TELECOMMUNICATIONS	10	5,079.29	4,982.94	-1.90	1	149.15	158.72	60- 60
12	URBAN DEVELOPMENT	5	73,993.32	79,266.22	7.13	0	0.00	0.00	0- 0
13	WATER RESOURCES	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		710	924307.04	1103914.08	19.43	87	173345.02	277659.29	

List of projects completed/dropped/Frozen during current month							(All Cost /Expenditure in Rs. crore)
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>PETROLEUM</u>						
1	IOR LAKWA - LAKHMANI (ONGCL)	09/2001	345.10	03/2007	750.00	03/2014	743.72
2	IOR GELEKI (ONGCL)	09/2001	390.09	03/2007	1,674.11	03/2017	1,759.52
3	IOR, RUDRASAGAR (ONGCL)	09/2001	113.90	03/2006	480.00	03/2014	452.91
4	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY	04/2008	825.00	04/2013	1,827.00	03/2014	1,545.00
5	DEVELOPMENT OF BHE AND BH-35 AREA.	08/2010	372.11	03/2013	372.11	02/2014	334.31
6	BUTENE-1 PROJECT AT PANIPAT	02/2012	190.00	03/2014	172.38	03/2014	125.28
7	DEVELOPMENT OF SB-14 FIELD	01/2011	410.44	11/2012	410.44	03/2014	337.16
8	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH	01/2007	740.02	03/2010	740.02	02/2014	739.83
	<u>POWER</u>						
9	EASTERN REGION STRENGTHENING SCHEME-I	10/2006	975.96	10/2009	975.96	N.A.	.00
10	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX	10/2010	182.68	01/2013	182.68	N.A.	.00
11	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VELLUR TPS	08/2010	170.36	04/2013	170.36	N.A.	.00
12	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUB STATION AT KALA IN UT DNH	07/2011	181.93	07/2013	181.93	N.A.	.00
13	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV	02/2009	520.48	11/2011	520.48	07/2014	.00
	<u>RAILWAYS</u>						
14	LANJHIGARH-JUNAGARH NL(ECOR)	04/1993	100.00	03/2002	227.94	02/2014	243.27

List of projects added					(All Cost in Rs. crore)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>PETROLEUM</u>					
1	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	5/2013	4,124.35	4/2016	4,124.35	4/2016
2	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE	4/2013	284.82	4/2015	284.82	4/2015

Milestones (Cumulative due & achieved)		
Total	3405	
Achieved up to month	1411	


List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>CIVIL AVIATION</u>						
1	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) AAI	335.61	388.53	05/2012	03/2014	04/2014	1
	<u>COAL</u>						
2	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) NLC	2,030.78	3,027.59	06/2009	05/2014	06/2014	1
	<u>STEEL</u>						
3	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) NMDC	295.89	607.17	12/2011	09/2014	01/2015	4
	<u>PETROLEUM</u>						
4	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 ONGC	5,713.03	8,813.41	05/2010	03/2014	05/2014	2
5	DEVELOPMENT OF B-46 CLUSTER FIELD ONGC	1,436.21	1,456.96	07/2010	03/2014	05/2014	2
6	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II ONGC	7,133.39	7,133.39	09/2012	03/2014	05/2014	2
7	102 MW WIND POWER PROJECT ONGC	1,106.00	678.02	06/2012	05/2014	07/2014	2
8	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG OIL	270.00	270.00	12/2014	08/2015	10/2015	2
9	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA GAIL	8,140.00	8,140.00	02/2014	03/2014	06/2014	3
10	POLYPROPYLENE UNIT MANGALORE REFIN	1,803.78	1,803.78	07/2012	03/2014	06/2014	3
11	MRPL PHASE-III EXPANSION MANGALORE REFIN	12,412.00	12,160.26	01/2012	03/2014	06/2014	3
12	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT OIL	144.02	204.29	06/2012	03/2014	06/2014	3
13	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY HPCL	3,597.00	2,730.00	09/2011	03/2014	07/2014	4
14	CREATION OF SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND ETP AT MADHUBAN OIL	374.56	374.56	09/2012	10/2016	03/2017	5
15	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY HPCL	3,284.00	2,174.00	09/2011	05/2014	12/2014	7

List of projects reporting additional delays


Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
16	CONSTRUCTION OF SIX EFFLUENT TREATMENT PLANTS (ETP), AHMEDABAD AND ANKLESWAR ONGC	234.78	317.64	09/2012	09/2013	12/2014	15
17	DEV OF G1 AND GS-15 (ONGCL) ONGC	429.82	2,735.65	04/2006	06/2014	06/2016	24
	<u>POWER</u>						
18	BARH STPP STAGE -II NTPC	7,341.04	7,341.04	08/2013	02/2015	03/2015	1
19	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME PGCIL	965.58	965.58	11/2012	03/2014	04/2014	1
20	BONGAIGAON THERMAL POWER PROJECT NTPC	4,375.35	4,375.35	07/2011	06/2016	08/2016	2
21	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) PGCIL	213.78	213.78	03/2014	03/2014	06/2014	3
22	PARBATI H.E.P. STAGE -III (NHPC) NHPC	2,304.56	2,716.00	10/2010	03/2014	08/2014	5
	<u>RAILWAYS</u>						
23	PANVEL PEN DOUBLING CR	191.00	260.16	N.A.	03/2014	05/2014	2
24	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) RVNL	2,298.42	2,298.42	03/2014	03/2014	03/2016	24
25	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT NEFR	283.55	283.55	N.A.	03/2015	03/2017	24
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
26	BRAHMPUTRA BRIDGE, NH NO-31 NHAI	217.61	309.56	04/2010	09/2015	01/2016	4
	<u>SHIPPING AND PORTS</u>						
27	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL MUMBAI PORT TRU	1,228.00	2,158.16	12/2010	03/2015	10/2015	7
	<u>TELECOMMUNICATIONS</u>						
28	SUPPLY INSTALLATION TESTING AND COMMISSIONING OF RURAL WIMAX NETWORK PHASE-II BSNL	1,148.19	964.37	05/2011	03/2014	05/2014	2
29	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTANCHAL BSNL	149.15	158.72	06/2009	03/2014	06/2014	3

List of projects reporting additional delays							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
30	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G BSNL	336.81	336.81	01/2009	03/2014	06/2014	3

Graphical Presentation of All Projects w.r.t. Original Schedule

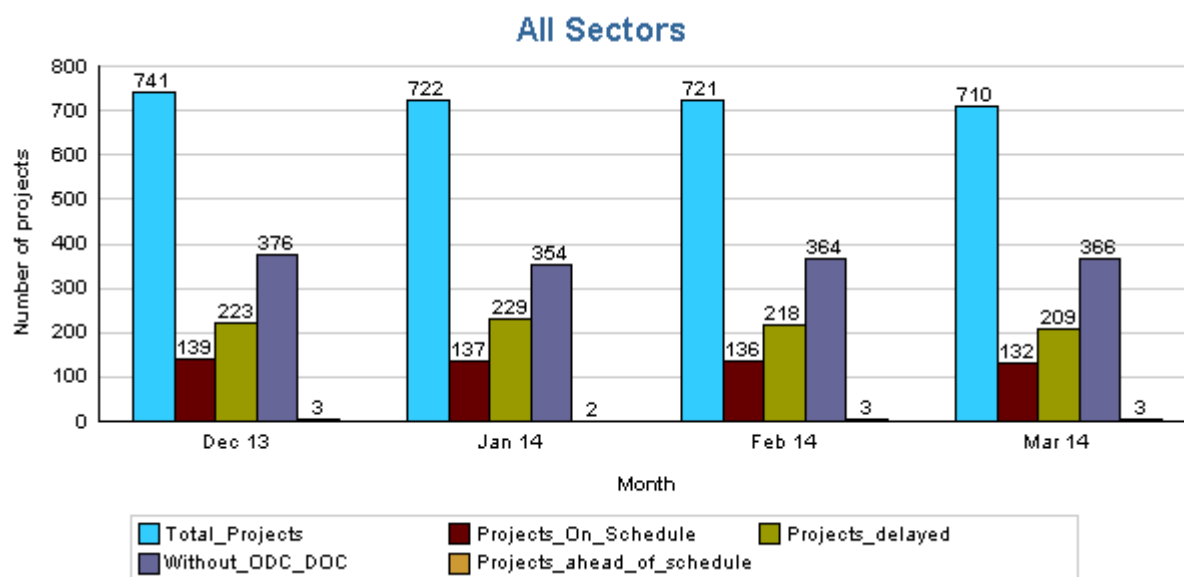

Break-up of 209 Delayed projects in March 2014

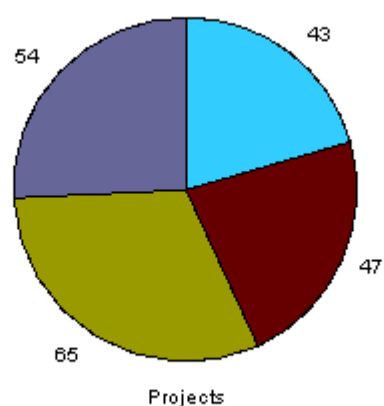


Delay in Months


Legend:

- 1-12
- 13-24
- 25-60
- MORE THAN 60

Graphical Presentation of All Projects w.r.t. Revised Schedule

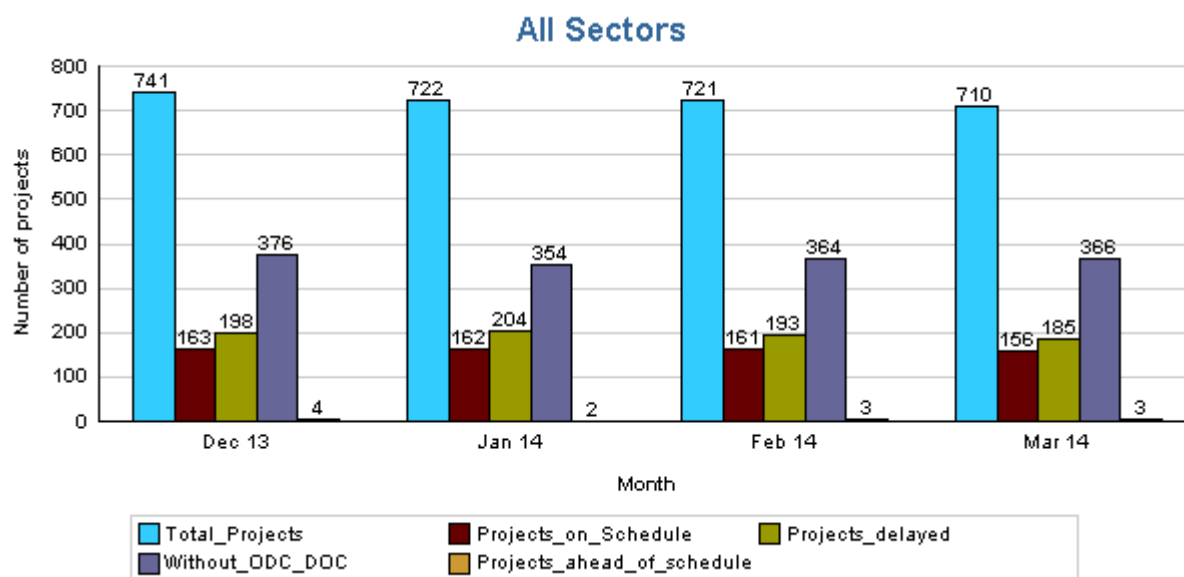


Break-up of 185 Delayed projects in March 2014

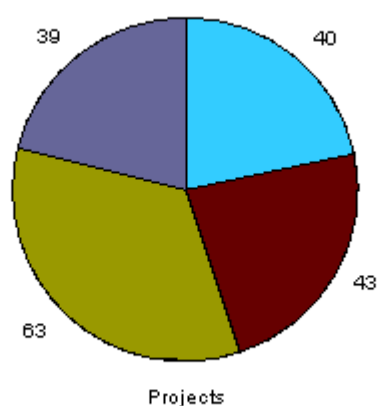


Delay in Months



Graphical Presentation of URBAN DEVELOPMENT Sector

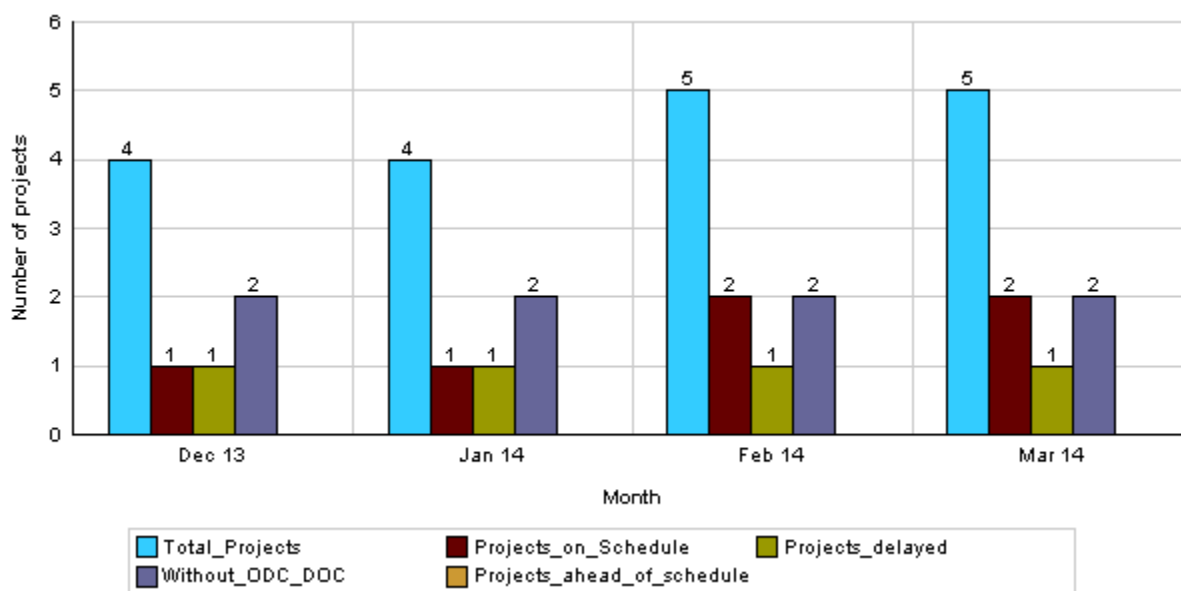


Break-up of 1 Delayed projects in March 2014




Delay in Months

Graphical Presentation of TELECOMMUNICATIONS Sector

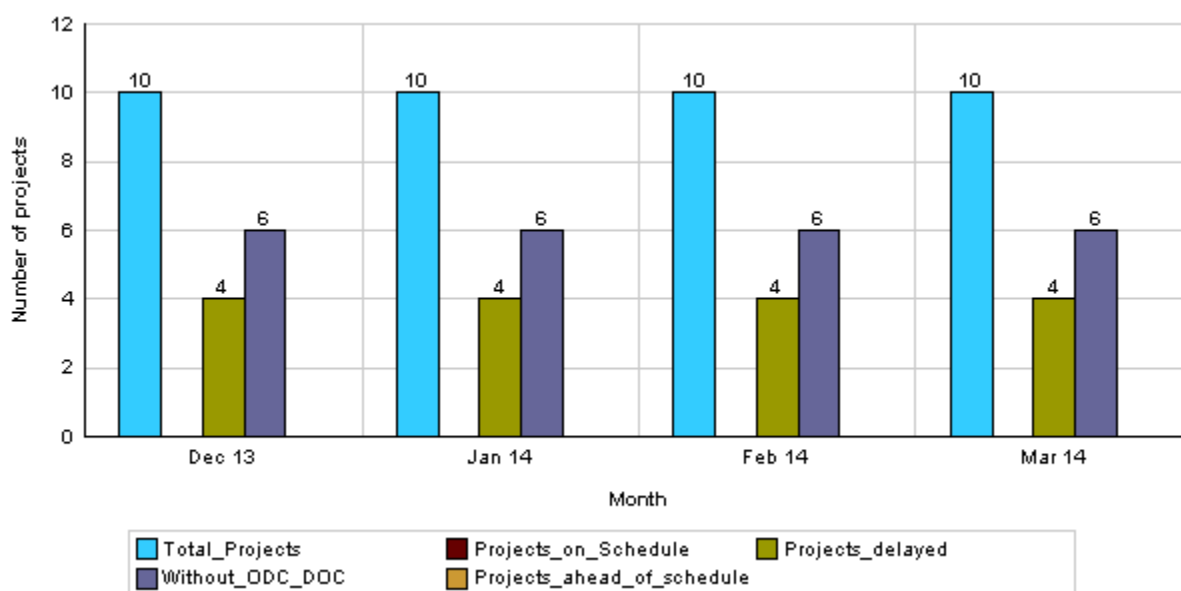


Break-up of 4 Delayed projects in March 2014

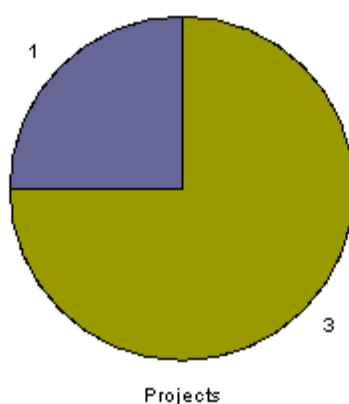


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	0	0	3	1

Graphical Presentation of SHIPPING AND PORTS Sector

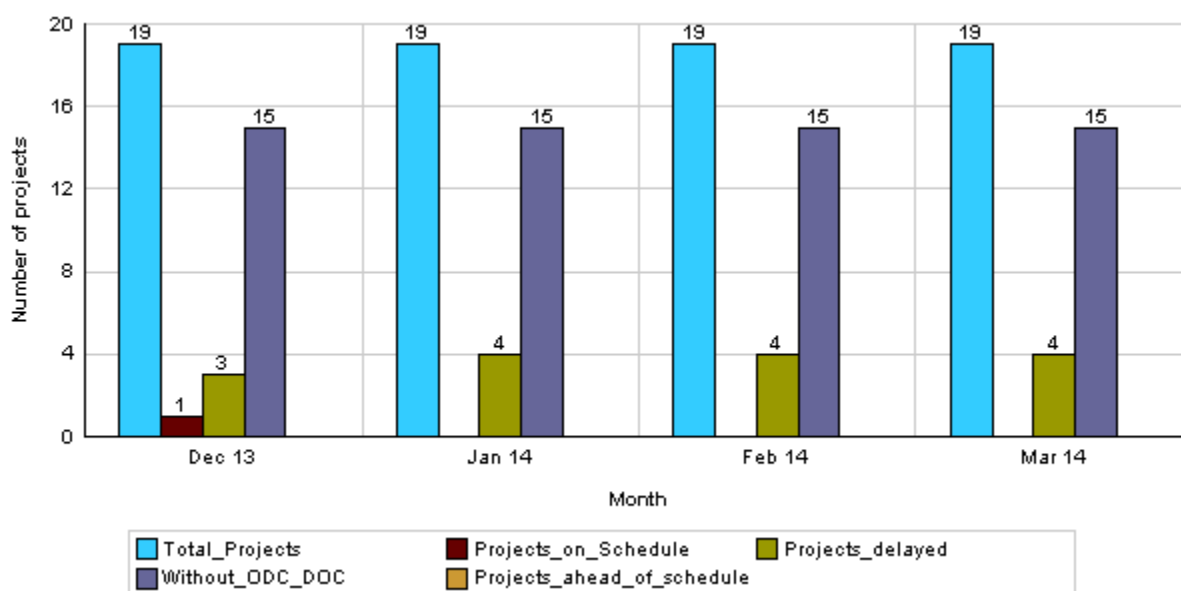


Break-up of 4 Delayed projects in March 2014

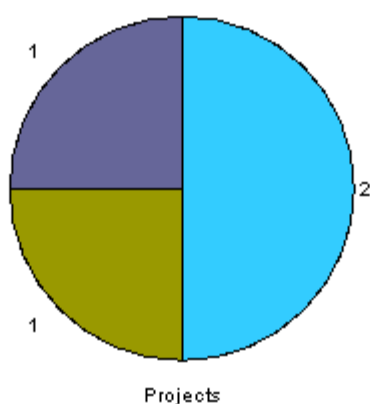


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	2	0	1	1

Graphical Presentation of ROAD TRANSPORT AND HIGHWAYS Sector

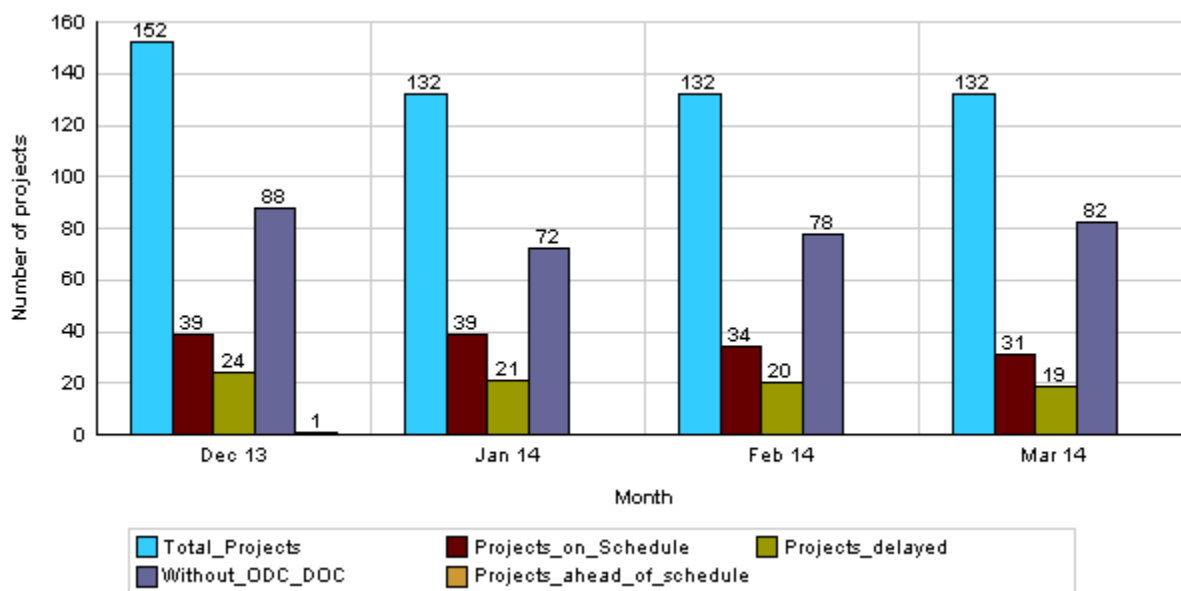


Break-up of 19 Delayed projects in March 2014

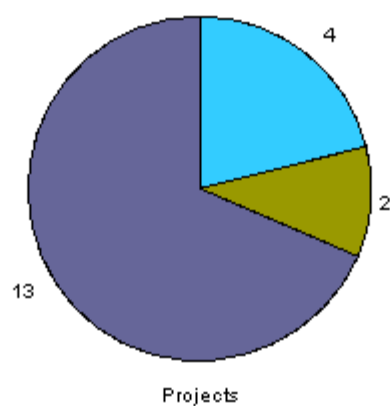


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	4	2	13	0

Graphical Presentation of RAILWAYS Sector

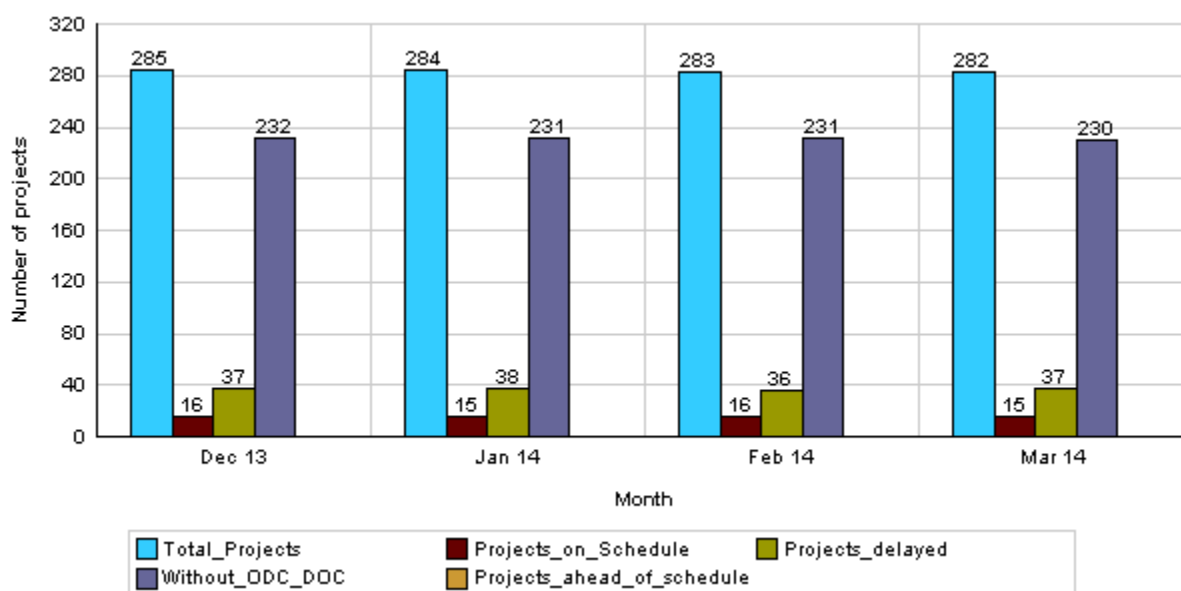


Break-up of 37 Delayed projects in March 2014

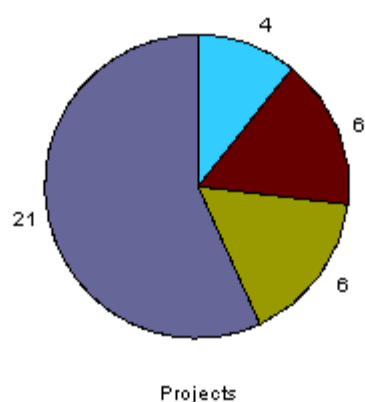


Delay in Months: 1-12 (Cyan), 13-24 (Dark Red), 25-60 (Olive Green), MORE THAN 60 (Purple)

Graphical Presentation of POWER Sector

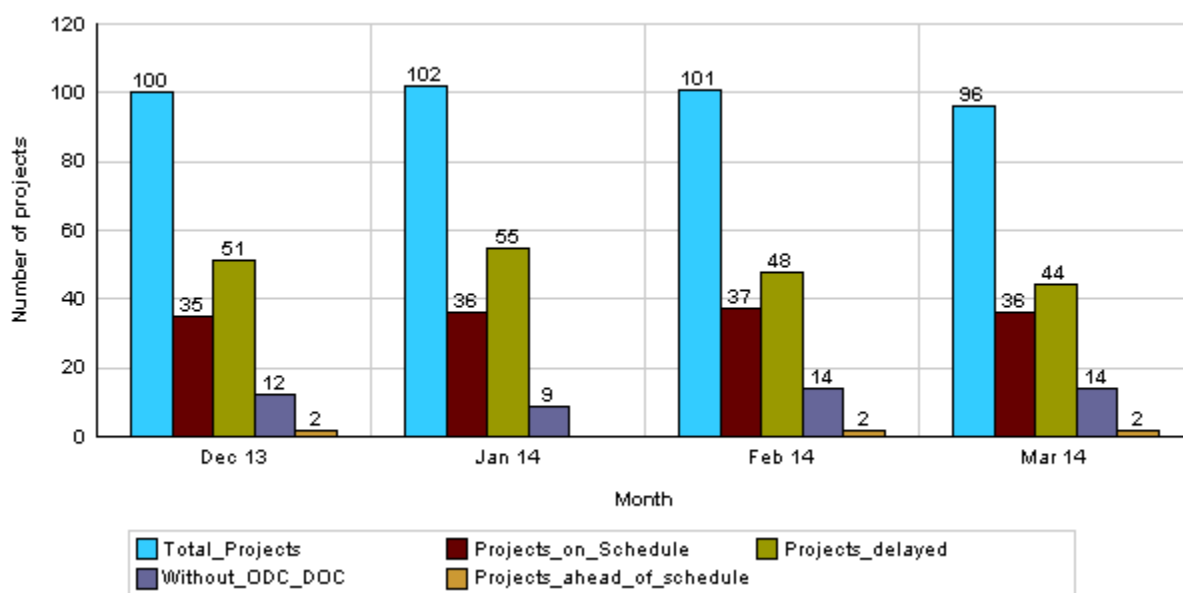


Break-up of 44 Delayed projects in March 2014

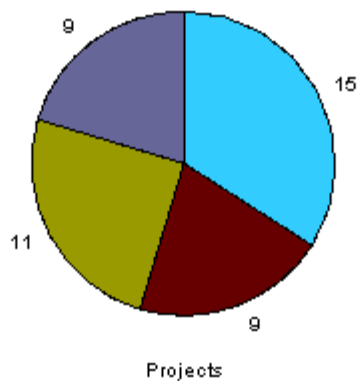


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of PETROLEUM Sector

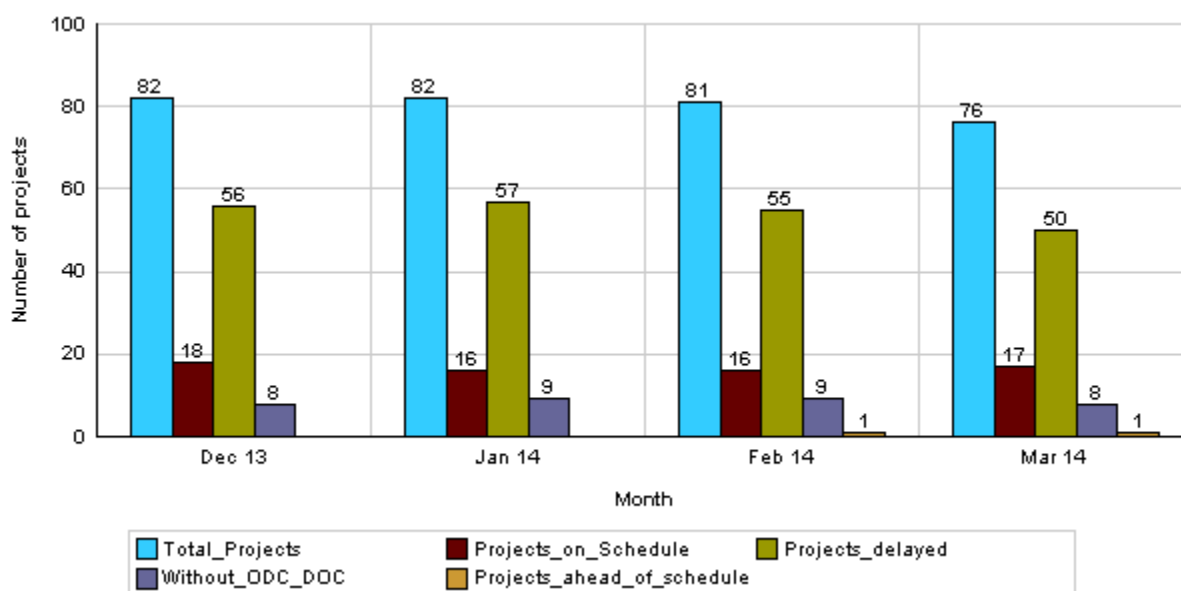


Break-up of 50 Delayed projects in March 2014

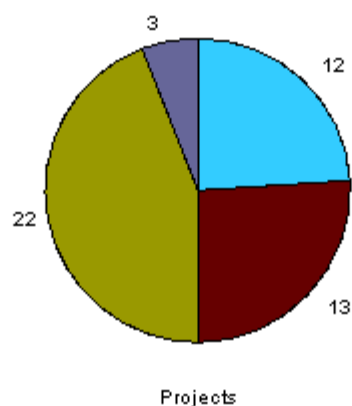


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of STEEL Sector

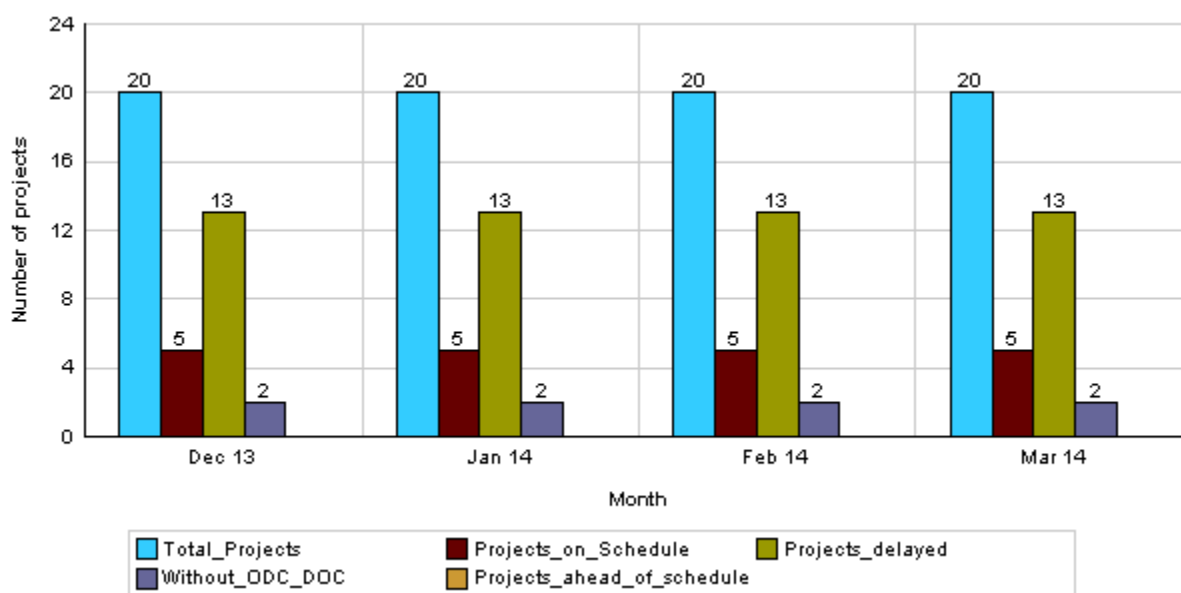


Break-up of 13 Delayed projects in March 2014

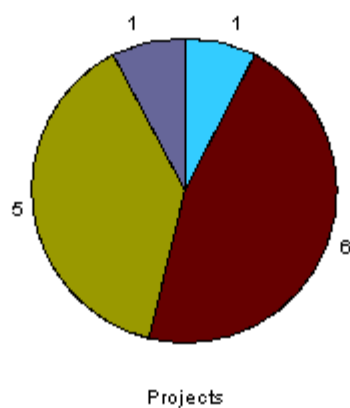


Delay in Months

Delay in Months	Count
1-12	1
13-24	6
25-60	5
MORE THAN 60	1

Graphical Presentation of COAL Sector

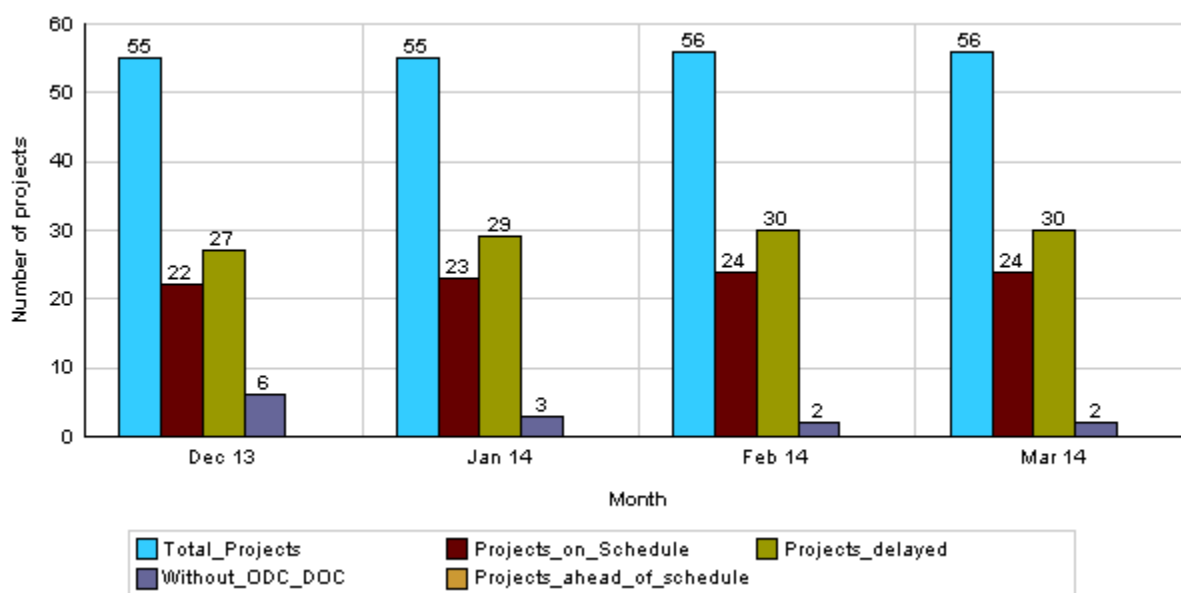


Break-up of 30 Delayed projects in March 2014

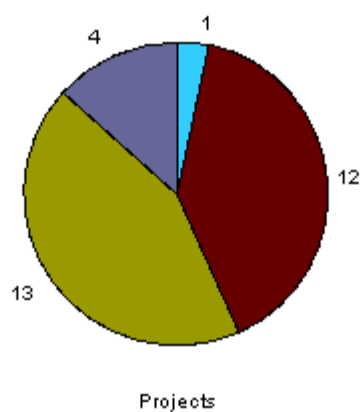


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Projects	1	12	13	4

Graphical Presentation of CIVIL AVIATION Sector

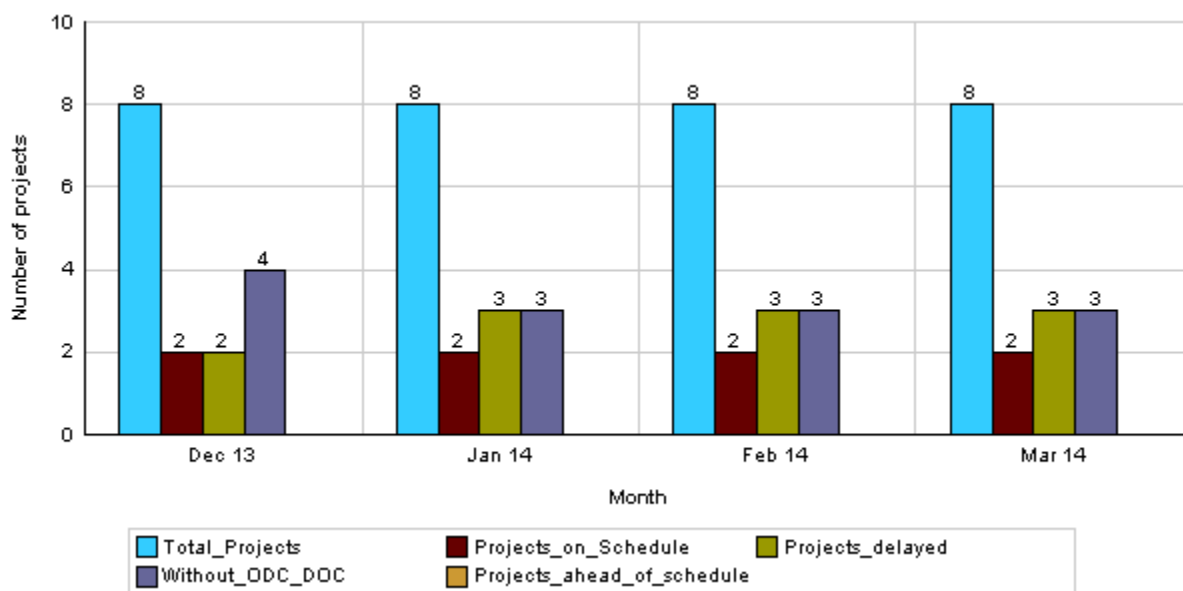


Break-up of 3 Delayed projects in March 2014

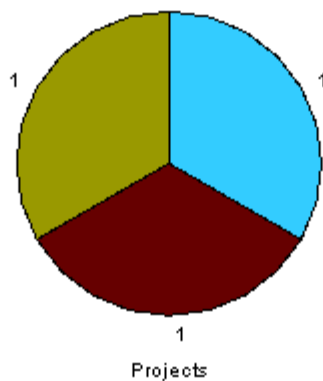


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	1	0	0	0
13-24	0	1	0	0
25-60	0	0	1	0
MORE THAN 60	0	0	0	1

Graphical Presentation of ATOMIC ENERGY Sector

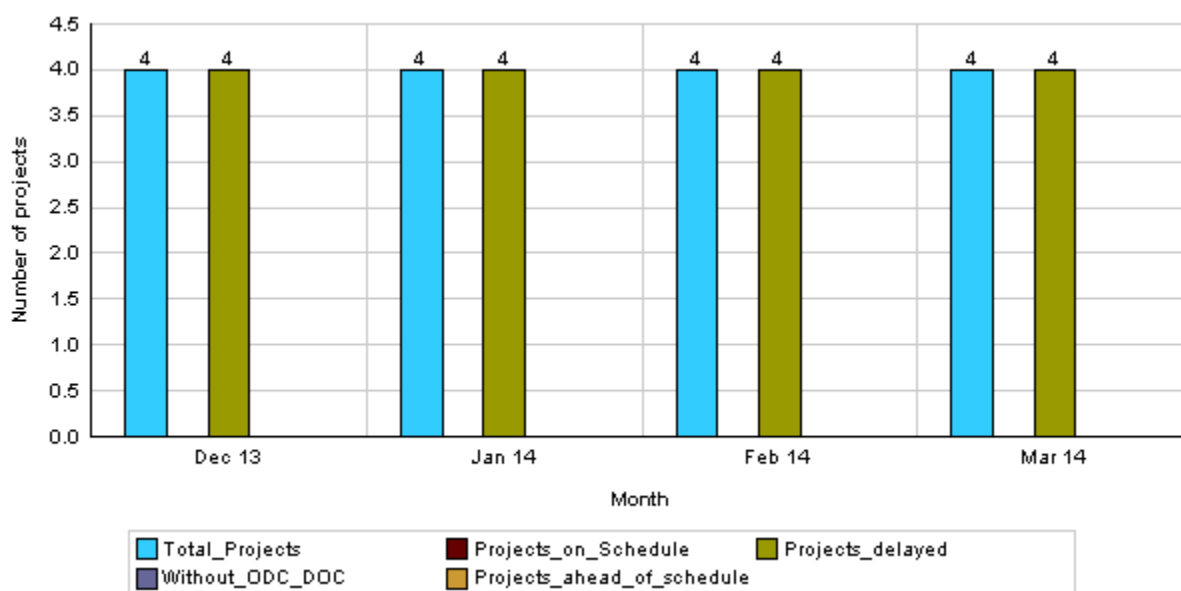

Break-up of 4 Delayed projects in March 2014

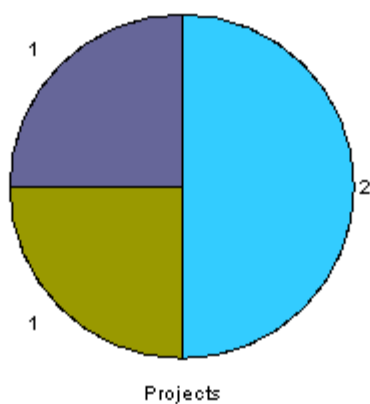

Delay in Months

Legend:

- 1-12
- 13-24
- 25-60
- MORE THAN 60

Sectorwise analysis of projects					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	40,442.00	40,442.00	46,726.00	17,198.00
CIVIL AVIATION	8	6,035.46	6,624.95	6,946.00	5,738.35
COAL	56	38,737.38	48,533.93	48,559.52	17,818.73
STEEL	20	65,959.26	70,209.44	72,188.55	59,215.71
PETROCHEMICALS	1	5,460.61	5,460.61	8,920.00	7,671.12
PETROLEUM	76	182,981.12	194,953.99	197,259.22	100,869.68
POWER	96	244,469.88	250,470.17	263,493.12	114,382.25
RAILWAYS	282	148,551.55	179,685.20	257,231.72	77,727.25
ROAD TRANSPORT AND HIGHWAYS	132	96,437.15	97,339.92	98,553.21	80,641.13
SHIPPING AND PORTS	19	15,617.12	17,487.95	18,600.58	8,807.06
TELECOMMUNICATIONS	10	5,079.29	5,079.29	4,982.94	1,767.57
URBAN DEVELOPMENT	5	73,993.32	74,052.22	79,266.22	9,926.37
WATER RESOURCES	1	542.90	542.90	1,187.00	35.49
Grand total	710	924,307.04	990,882.57	1,103,914.08	501,798.71

(All Cost/ Expenditure in Rs. Crore)

Sector Wise Details									
(March 2014)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	-	12/2015 -	11/2016	11(O) -	4/70
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00 -	17,270.00	17,198.00	12/2008 -	12/2014	72(O) -	40/102
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 -	5,677.00	-	09/2010 -	03/2015	54(O) -	12/88
4	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	-	12/2016 -	03/2017	3(O) -	4/69
	Total		40,442.00 -	46,726.00	17,198.00				60/329
	<u>CIVIL AVIATION</u>								
5	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,WEST BENGAL	08/2008	1,942.51 2,325.00	2,593.13	2,537.92	05/2011 -	03/2013	-	0/2
6	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	309.46	269.55	01/2011 04/2013	03/2015	50(O) 23(R)	0/0
7	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 335.61	388.53	278.32	05/2012 -	04/2014	23(O) -	0/0
8	D/O KAMARAJ DOMESTIC TER-PH-II AND EXP. ANNA INT. TER BLDG(K1) - [N04000038]AAI,TAMIL NADU	08/2008	1,808.00 2,015.00	2,015.00	1,938.97	01/2011 02/2012	02/2012	-	0/0
9	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]AAI,CHANDIGARH	02/2011	452.00 -	452.00	230.42	03/2015 -	03/2015	0(O) -	0/0
10	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	344.28	-	03/2014 -	10/2014	7(O) -	0/0
11	GAGAN PROJECT - [N04000065]AAI,MULTI STATE	09/2008	626.00 -	626.00	483.13	06/2013 -	06/2013	-	0/0
12	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	217.60	0.04	03/2015 -	03/2015	0(O) -	0/0
	Total		6,035.46 -	6,946.00	5,738.35				0/2
	<u>COAL</u>								
13	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,ANDHRA PRADESH	12/2009	212.34 1,228.39	1,228.39	1,206.66	03/2013 09/2012	03/2015	24(O) 30(R)	18/22
14	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH	11/2009	150.59 -	198.59	90.43	03/2016 -	03/2016	0(O) -	2/7
15	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]NCL,MADHYA PRADESH	12/2009	1,352.04 1,143.54	1,143.54	613.44	03/2016 03/2016	03/2016	0(O) 0(R)	0/4
16	AMRAPALI OC(12MTY) - [N06000103]CCL,JHARKHAND	02/2012	858.11 -	858.11	67.22	03/2020 -	03/2020	0(O) -	0/3

Sector Wise Details

(March 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
17	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	126.88	03/2012 -	03/2016	48(O) -	5/6
18	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	471.66 341.63	341.63	119.71	03/2011 -	03/2014	36(O) -	0/2
19	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	131.62	03/2010 -	03/2016	72(O) -	3/4
20	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56 -	258.56	55.25	03/2016 -	03/2016	0(O) -	0/6
21	BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH	09/2008	203.82 -	203.82	-	03/2015 -	03/2015	0(O) -	1/6
22	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.00 -	490.10	160.06	03/2017 -	03/2017	0(O) -	4/12
23	BINA EXTN. PROJ(6.0 MTPA) - [N06000019]NCL,MULTI STATE	11/2006	168.97 -	168.97	44.08	03/2014 -	03/2014	0(O) -	0/2
24	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,MADHYA PRADESH	06/2011	746.04 -	535.10	222.53	03/2015 -	03/2015	0(O) -	0/3
25	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH	12/2013	610.33 -	610.33	-	03/2022 -	03/2022	0(O) -	0/0
26	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35 -	462.35	270.85	03/2014 -	03/2016	24(O) -	2/8
27	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	35.38	03/2011 -	03/2016	60(O) -	0/2
28	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,345.03	03/2014 -	03/2016	24(O) -	6/12
29	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,632.11	03/2014 -	03/2016	24(O) -	10/15
30	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,ODISHA	02/2008	395.87 -	395.87	75.42	03/2015 -	03/2015	0(O) -	1/13
31	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.63 -	479.63	120.15	03/2013 -	03/2015	24(O) -	3/8
32	JAGANNATHPOR OC - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	152.43	-	03/2015 -	03/2017	24(O) -	1/7
33	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,ANDHRA PRADESH	07/2011	447.06 -	447.06	29.04	03/2015 -	03/2015	0(O) -	4/31
34	JALLARAM SHAFT PROJECT - [N06000025]SCCL,ANDHRA PRADESH	09/2007	467.78 -	467.78	12.31	03/2013 -	-	-	6/83
35	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL	11/2006	287.18 -	287.17	36.31	03/2011 -	03/2017	72(O) -	0/2
36	KAKATIYA LONGWALL - [N06000048]SCCL,ANDHRA PRADESH	12/2008	453.63 -	453.63	102.23	12/2012 -	03/2016	39(O) -	10/44
37	KALYANIKHANI OPENCASE PROJECT - [N06000101]SCCL,ANDHRA PRADESH	07/2012	417.33 -	417.33	0.24	07/2016 -	07/2016	0(O) -	3/39
38	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	116.72	03/2013 -	03/2015	24(O) -	5/10
39	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	55.85	03/2014 -	03/2014	0(O) -	0/2
40	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24(O) -	1/7
41	KHADIA EXPANSION OPENCASE PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]NCL,UTTAR PRADESH	06/2011	1,131.28 -	1,131.28	19.19	03/2018 -	03/2018	0(O) -	0/4

Sector Wise Details

(March 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
42	KISTARAM OCP - [N06000089]SCCL,ANDHRA PRADESH	11/2010	242.29 -	242.29	-	03/2015 -	03/2015	0(O) -	0/28
43	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,UTTAR PRADESH	06/2011	789.88 -	741.62	388.56	03/2013 -	03/2014	12(O) -	0/2
44	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	118.59	03/2010 -	03/2017	84(O) -	9/10
45	KUSMUNDA EXPN.OCP(SECL)(10-15)MTY - [N06000008]SECL,CHHATISGARH	06/2008	1,188.31 7,612.33	7,612.33	747.82	03/2013 03/2023	03/2023	120(O) 0(R)	0/9
46	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	469.78 -	706.40	32.17	07/2012 -	03/2016	44(O) -	0/3
47	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.42 -	321.50	213.59	03/2014 -	03/2016	24(O) -	1/6
48	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,ANDHRA PRADESH	03/2010	181.19 -	181.19	35.35	03/2012 -	03/2015	36(O) -	4/6
49	MOONIDH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015	0(O) -	0/0
50	MURADH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	-	04/2014 -	04/2014	0(O) -	0/0
51	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 -	5,907.11	339.15	12/2015 -	04/2018	28(O) -	5/33
52	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 -	259.40	6.99	03/2012 -	03/2015	36(O) -	0/2
53	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	63.66	03/2012 -	03/2017	60(O) -	0/2
54	PELMA OCP(10.00MTY) - [N06000045]SECL,CHHATISGARH	07/2008	448.32 -	448.32	-	03/2015 -	03/2015	0(O) -	1/1
55	PENGANGA OC - [N06000066]WCL,MAHARASHTRA	10/2008	339.77 -	339.77	2.30	03/2014 -	03/2016	24(O) -	0/1
56	PURNADH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	123.07	03/2013 -	03/2015	24(O) -	0/3
57	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	33.46	03/2014 -	03/2016	24(O) -	0/2
58	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	268.01	03/2016 -	03/2016	0(O) -	0/2
59	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,ANDHRA PRADESH	12/2009	418.97 -	418.97	240.26	03/2012 -	03/2015	36(O) -	24/27
60	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,ANDHRA PRADESH	07/2011	162.76 -	162.76	2.56	03/2015 -	03/2015	0(O) -	4/29
61	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,ANDHRA PRADESH	11/2012	430.14 -	430.14	65.48	03/2016 -	03/2016	0(O) -	5/48
62	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,ANDHRA PRADESH	06/2012	365.01 -	365.01	5.43	06/2015 -	06/2015	0(O) -	2/51
63	RKP OCP PHASE-I - [N06000079]SCCL,ANDHRA PRADESH	03/2010	209.78 -	209.78	93.46	03/2015 -	03/2015	0(O) -	8/31
64	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,ANDHRA PRADESH	10/2006	249.03 -	249.03	61.70	03/2012 -	-	-	22/42
65	TALABIRA OCP - [N06000043]MCL,ODISHA	03/2008	447.72 -	447.72	50.46	03/2016 -	03/2016	0(O) -	0/12
66	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	141.89	03/2012 -	03/2016	48(O) -	0/2

Sector Wise Details

(March 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
67	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,TAMIL NADU	10/2004	2,030.78 3,027.59	3,027.59	2,904.44	06/2009 -	06/2014	60(O) -	19/23
68	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	5,191.62	03/2012 -	08/2014	29(O) -	19/38
	Total		38,737.38 -	48,559.52	17,818.73				208/777
	STEEL								
69	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,KARNATAKA	04/2011	572.00 -	572.00	379.62	04/2013 09/2014	09/2014	17(O) 0(R)	17/18
70	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND	10/2013	245.67 -	245.67	6.91	05/2016 -	05/2016	0(O) -	0/3
71	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,ANDHRA PRADESH	08/2006	260.00 349.64	349.64	259.71	12/2009 08/2010	06/2013	-	1/1
72	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT EXP. UNIT - [N12000068]RINL,ANDHRA PRADESH	07/2007	202.00 343.58	343.58	290.19	01/2010 02/2011	11/2013	-	3/3
73	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,KARNATAKA	02/2011	898.55 -	898.55	291.82	05/2013 01/2015	01/2015	20(O) 0(R)	13/20
74	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]RINL,MULTI STATE	07/2007	480.00 -	450.00	309.45	09/2009 05/2012	07/2014	58(O) 26(R)	1/1
75	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]NMDC,CHHATISGARH	01/2007	295.89 607.17	607.17	369.58	12/2011 01/2015	01/2015	37(O) 0(R)	15/20
76	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,ANDHRA PRADESH	06/2006	108.00 216.68	216.68	160.46	09/2008 12/2013	04/2014	67(O) 4(R)	3/4
77	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHHATISGARH - [N12000078]SAIL,CHHATISGARH	07/2012	332.65 -	332.65	102.39	08/2014 -	08/2014	0(O) -	1/2
78	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL,ODISHA	11/2011	254.55 -	254.55	104.16	11/2013 -	06/2015	19(O) -	1/3
79	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	12,491.86	03/2013 -	03/2015	24(O) -	28/32
80	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,JHARKHAND	05/2010	6,325.00 -	6,325.00	4,591.34	12/2011 -	03/2014	27(O) -	18/21
81	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,WEST BENGAL	08/2010	2,875.00 -	2,875.00	2,153.22	12/2012 -	12/2014	24(O) -	14/16
82	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,WEST BENGAL	06/2008	14,443.00 -	16,408.00	15,787.87	12/2011 -	06/2014	30(O) -	22/23
83	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL,ANDHRA PRADESH	10/2005	8,692.00 12,291.00	12,291.00	10,792.31	10/2009 10/2012	07/2014	57(O) 21(R)	66/67
84	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]SAIL,ODISHA	08/2010	11,812.00 -	11,812.00	10,870.17	03/2013 -	09/2014	18(O) -	16/19
85	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA	12/2011	187.33 -	187.33	119.88	10/2013 -	08/2014	10(O) -	0/3
86	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL,ODISHA	10/2012	160.48 -	160.48	18.86	09/2014 -	09/2014	0(O) -	0/2
87	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]SAIL,WEST BENGAL	11/2012	313.05 -	339.35	83.98	06/2015 -	06/2015	0(O) -	1/2

Sector Wise Details

(March 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
88	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079]SAIL,ODISHA	06/2012	237.09 -	254.90	31.93	12/2014 -	12/2014	0(O) -	0/1
	Total		65,959.26 -	72,188.55	59,215.71				220/261
	<u>PETROCHEMICALS</u>								
89	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,ASSAM	04/2006	5,460.61 -	8,920.00	7,671.12	04/2012 -	-	-	19/29
	Total		5,460.61 -	8,920.00	7,671.12				19/29
	<u>PETROLEUM</u>								
90	102 MW WIND POWER PROJECT - [N16000119]ONGC,RAJASTHAN	07/2010	1,106.00 -	678.02	77.45	06/2012 -	07/2014	25(O) -	0/4
91	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,MULTI STATE	01/2010	2,163.64 2,331.62	2,331.62	1,889.99	06/2012 -	05/2014	23(O) -	0/0
92	AHMEDABAD REDEVELOPMENT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10 -	1,916.10	784.46	12/2014 -	12/2016	24(O) -	0/0
93	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63 -	2,189.63	1,039.42	12/2014 -	12/2016	24(O) -	0/0
94	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 -	2,378.89	1,496.19	03/2013 03/2014	03/2015	24(O) 12(R)	0/5
95	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]OCL,MULTI STATE	08/2011	586.00 -	586.00	160.16	08/2015 -	08/2015	0(O) -	0/0
96	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,MULTI STATE	12/2009	540.92 -	540.92	336.28	07/2012 07/2012	-	-	6/7
97	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,ASSAM	08/2008	144.02 -	204.29	154.08	06/2012 -	06/2014	24(O) -	0/0
98	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	736.65	448.92	09/2011 -	12/2014	39(O) -	0/0
99	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC,MULTI STATE	11/2010	331.20 -	331.20	164.19	08/2013 -	09/2014	13(O) -	0/5
100	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	302.26 -	240.95	102.78	09/2012 -	12/2014	27(O) -	0/0
101	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 -	202.94	2.00	01/2014 -	01/2015	12(O) -	0/5
102	CONSTRUCTION OF ONE ETP AT GGS-NADA, ANKLESHWAR - [N16000134]ONGC,GUJARAT	10/2011	200.69 -	200.69	8.08	07/2014 -	03/2015	8(O) -	0/5
103	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	723.64	-	03/2013 -	06/2016	39(O) -	0/0
104	CONSTRUCTION OF SIX EFFLUENT TREATMENT PLANTS (ETP), AHMEDABAD AND ANKLESWAR - [N16000099]ONGC,GUJARAT	03/2009	234.78 234.78	317.64	102.78	09/2012 -	12/2014	27(O) -	0/5
105	CONSTRUCTION OF THREE ETPS, MEHSANA - [N16000135]ONGC,GUJARAT	03/2012	260.74 -	260.74	0.52	11/2014 -	11/2015	12(O) -	0/5
106	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 -	861.79	495.39	05/2013 06/2014	06/2014	13(O) 0(R)	0/5

Sector Wise Details

(March 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
107	CREATION OF SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND ETP AT MADHUBAN - [N16000167]OIL,MULTI STATE	08/2006	374.56 -	374.56	10.60	09/2012 -	03/2017	54(O) -	0/0
108	DABHOL BANGALORE PIPELINE PROJECT PHASE-II - [N16000147]GAIL,MULTI STATE	06/2009	486.00 -	486.00	91.99	09/2013 -	09/2013	-	0/1
109	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA	12/2009	1,584.00 -	1,584.00	795.25	- -	-	-	0/1
110	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,MULTI STATE	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	06/2016	122(O) 48(R)	0/0
111	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,MAHARASHTRA	06/2007	3,248.78 5,633.44	5,633.44	5,190.51	08/2010 03/2012	05/2014	45(O) 26(R)	0/10
112	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,MAHARASHTRA	01/2007	2,323.40 2,920.82	2,920.82	1,915.45	09/2010 03/2012	12/2015	63(O) 45(R)	0/0
113	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,MAHARASHTRA	06/2007	1,436.21 1,456.96	1,456.96	1,100.32	07/2010 05/2012	05/2014	46(O) 24(R)	0/0
114	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 -	2,592.17	234.78	05/2014 -	05/2015	12(O) -	0/9
115	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,MAHARASHTRA	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	09/2014	69(O) 17(R)	0/0
116	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]ONGC,MULTI STATE	03/2010	3,241.03 5,916.65	6,638.94	1,451.42	03/2013 11/2014	11/2014	20(O) 0(R)	0/10
117	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC,MULTI STATE	04/2013	284.82 -	284.82	-	04/2015 -	04/2015	0(O) -	0/0
118	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17 -	600.17	219.43	12/2014 -	12/2014	0(O) -	0/8
119	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE	06/2010	2,523.00 -	2,523.00	1,002.33	01/2014 -	12/2015	23(O) -	0/9
120	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,MAHARASHTRA	03/2009	3,284.00 2,174.00	2,174.00	1,881.89	09/2011 05/2012	12/2014	39(O) 31(R)	6/76
121	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,ANDHRA PRADESH	03/2009	3,597.00 2,730.00	2,730.00	2,061.74	09/2011 03/2012	07/2014	34(O) 28(R)	56/59
122	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	711.00	2.29	- -	-	-	0/0
123	FIRE WATER NETWORK AT URAN - [N16000141]ONGC,MAHARASHTRA	05/2010	171.68 -	171.68	96.43	06/2013 -	05/2014	11(O) -	0/5
124	GAS TURBINE GENERATION SET - [N18000146]OIL,ASSAM	07/2009	216.88 -	216.88	177.92	10/2011 -	06/2014	32(O) -	0/9
125	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]ONGC,MAHARASHTRA	03/2012	5,608.40 -	5,608.40	2,182.76	05/2015 -	05/2015	0(O) -	0/17
126	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	522.90	03/2015 -	03/2015	0(O) -	0/12
127	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]ONGC,MAHARASHTRA	12/2012	3,513.07 -	3,513.07	-	02/2016 -	02/2016	0(O) -	0/0
128	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE	05/2013	4,124.35 -	4,124.35	-	04/2016 -	04/2016	0(O) -	0/0
129	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL,KERALA	01/1999	14,225.00 -	14,225.00	1,814.37	12/2015 -	05/2016	5(O) -	0/0
130	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE	01/2012	352.49 -	352.49	84.56	03/2014 -	12/2014	9(O) -	0/5
131	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18 -	7,596.18	13.50	01/2013 -	12/2015	35(O) -	0/0

Sector Wise Details

(March 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
132	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,HARYANA	11/2007	281.07 -	281.07	4.42	10/2010 -	12/2014	50(O) -	0/0
133	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I - [N16000070]GAIL,MULTI STATE	07/2009	238.68 -	312.00	293.12	01/2012 -	07/2013	-	0/1
134	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00 -	2,300.00	1,287.26	12/2012 -	-	-	0/10
135	KOTA JOBNER PIPELINE PROJECT - [N16000170]BPCL,RAJASTHAN	04/2011	276.26 -	276.26	135.34	03/2015 -	03/2015	0(O) -	0/64
136	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	12/2012	607.06 -	607.06	20.38	01/2016 -	12/2015	-1(O) -	0/0
137	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,KARNATAKA	11/2012	666.00 701.00	701.00	202.33	11/2015 -	11/2015	0(O) -	18/29
138	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL,ODISHA	07/2009	199.75 -	199.75	133.42	06/2014 -	06/2014	0(O) -	0/0
139	MEHESANA REDEVELOPMENT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	3,823.00	1,076.07	04/2015 -	03/2017	23(O) -	0/0
140	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL,TAMIL NADU	12/2012	279.00 -	279.00	65.09	12/2014 -	12/2014	0(O) -	0/0
141	MRPL PHASE-III EXPANSION - [N16000114]MANGALORE REFIN,KARNATAKA	08/2008	12,412.00 -	12,160.26	11,518.36	01/2012 -	06/2014	29(O) -	0/108
142	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,MAHARASHTRA	01/2009	7,133.39 -	7,133.39	5,543.40	09/2012 -	05/2014	20(O) -	0/0
143	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,MAHARASHTRA	10/2007	5,713.03 8,813.41	8,813.41	7,351.12	05/2010 03/2013	05/2014	48(O) 14(R)	0/0
144	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	913.00	106.53	07/2015 -	07/2015	0(O) -	0/0
145	PARADIP REFINERY PROJECT - [N16000058]IOCL,ODISHA	02/2009	29,777.00 -	32,710.00	25,230.00	11/2012 -	12/2014	25(O) -	70/100
146	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	961.93	09/2012 -	08/2015	35(O) -	6/11
147	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,MULTI STATE	08/2010	8,140.00 -	8,140.00	6,422.66	02/2014 -	06/2014	4(O) -	0/0
148	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]BPCL,MAHARASHTRA	08/2009	246.81 -	276.83	258.57	04/2012 -	06/2014	26(O) -	0/0
149	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT	09/2011	202.25 -	202.25	33.26	07/2016 -	07/2016	0(O) -	0/5
150	PIPELINE REPLACEMENT PROJECT-3 - [N16000137]ONGC,MULTI STATE	04/2012	2,547.26 -	2,547.26	1,015.93	05/2014 -	05/2014	0(O) -	0/5
151	POLYPROPYLENE UNIT - [N16000113]MANGALORE REFIN,KARNATAKA	05/2009	1,803.78 -	1,803.78	884.59	07/2012 -	06/2014	23(O) -	0/31
152	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	270.00	-	12/2014 -	10/2015	10(O) -	0/0
153	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 -	1,138.50	33.92	04/2015 -	04/2015	0(O) -	0/0
154	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL,MAHARASHTRA	01/1999	1,419.00 -	1,419.00	409.10	12/2014 -	03/2015	3(O) -	0/0
155	REWARI KANPUR PIPELINE PROJECT - [N16000145]HPCL,MULTI STATE	02/2012	1,210.64 -	1,210.64	504.90	11/2015 -	11/2015	0(O) -	12/25

Sector Wise Details

(March 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
156	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]MANGALORE REFIN,KARNATAKA	07/2010	1,043.57 -	957.10	655.84	04/2012 -	12/2013	-	0/0
157	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	793.29	10/2011 -	06/2015	44(O) -	0/0
158	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,102.03	01/2012 -	06/2015	41(O) -	0/0
159	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,ANDHRA PRADESH	01/2006	672.00 1,038.00	1,038.00	936.55	10/2011 -	09/2014	35(O) -	0/0
160	SURAT PARADIP PIPELINE PROJECT - [N16000163]GAIL,MULTI STATE	10/2012	10,281.00 -	10,281.00	1.36	- -	04/2015	- -	0/0
161	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]ONGC,TRIPURA	07/2008	288.04 288.04	253.66	210.07	08/2012 -	06/2014	22(O) -	0/5
162	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	871.35	10.93	03/2015 -	03/2015	0(O) -	0/5
163	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	11/2012	309.81 -	309.82	67.83	10/2014 -	10/2015	12(O) -	0/0
164	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	330.47	270.05	03/2012 -	03/2016	48(O) -	13/20
165	WAX PROJECT - [N16000101]NRL,ASSAM	06/2010	576.60 -	676.05	511.99	12/2013 -	03/2014	3(O) -	0/0
	Total		182,981.12 -	197,259.22	100,869.68				187/696
	<u>POWER</u>								
166	765 KV POOLING STATION AND NETWORK WITH DVC AND MAITHOB RBC - [N18000069]PGCIL,MULTI STATE	08/2008	7,075.33 -	7,075.33	-	08/2012 -	03/2014	19(O) -	0/11
167	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]NEEPCO,TRIPURA	07/2012	296.87 -	296.87	173.77	- -	-	-	0/17
168	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]PGCIL,MULTI STATE	12/2012	156.04 -	156.04	24.39	10/2014 -	10/2014	0(O) -	0/7
169	BARH STPP STAGE -II - [N18000047]NTPC,BIHAR	02/2008	7,341.04 -	7,341.04	6,847.00	08/2013 -	03/2015	19(O) -	14/19
170	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	12/2003	8,692.97 -	8,693.00	9,238.00	12/2009 -	03/2017	87(O) -	24/49
171	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 -	4,375.35	4,311.00	07/2011 -	08/2016	61(O) -	6/28
172	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	23.38	12/2015 -	12/2015	0(O) -	2/20
173	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,272.71	09/2014 -	12/2014	3(O) -	7/20
174	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]PGCIL,ANDHRA PRADESH	06/2012	1,909.24 -	1,909.24	381.51	06/2015 -	06/2015	0(O) -	0/0

Sector Wise Details

(March 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
175	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNAM OF ANDHRA PRADESH(PGCIL) - [N18000111]PGCIL,ANDHRA PRADESH	08/2011	1,637.34 -	1,637.34	1,353.68	08/2014 -	08/2014	0(O) -	7/20
176	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,ANDHRA PRADESH	03/2012	206.44 -	206.44	42.57	06/2014 -	06/2014	0(O) -	0/20
177	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	-	06/2015 -	06/2015	0(O) -	0/0
178	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139]PGCIL,TAMIL NADU	01/2013	182.80 -	182.80	10.71	10/2014 -	10/2014	0(O) -	2/2
179	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	1,364.52	-	05/2016 -	05/2016	0(O) -	0/0
180	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	808.16	11/2012 -	06/2015	31(O) -	2/13
181	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	-	09/2014 -	09/2014	0(O) -	0/0
182	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATTISGARH	05/2011	1,961.87 -	1,961.87	-	05/2014 -	05/2014	0(O) -	2/8
183	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	02/2013	11,638.55 -	11,638.55	1,030.00	09/2017 -	09/2017	0(O) -	4/38
184	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,BIHAR	12/2011	901.77 -	901.77	598.30	08/2014 -	08/2014	0(O) -	1/16
185	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000107]PGCIL,CHHATTISGARH	08/2011	1,391.97 -	1,391.97	-	12/2013 -	-	-	2/7
186	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154]PGCIL,MAHARASHTRA	10/2013	1,315.90 -	1,315.90	-	11/2016 -	11/2016	0(O) -	0/0
187	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,KARNATAKA	03/2005	596.45 -	1,007.16	929.66	12/2007 12/2009	-	-	2/11
188	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 -	4,653.95	2,816.40	12/2009 06/2016	03/2017	87(O) 9(R)	11/26
189	KISHANGANGA HEP - [N18000031]NHPC,JAMMU AND KASHMIR	07/2007	2,238.67 3,642.04	3,642.00	3,283.02	01/2016 -	11/2016	10(O) -	0/6
190	KOLDAM HEP (NTPC) - [180100211]NTPC,HIMACHAL PRADESH	10/2002	4,527.15 7,220.00	7,220.00	5,687.00	04/2009 -	05/2015	73(O) -	1/9
191	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	12/2011	15,166.19 -	15,166.19	3,237.00	12/2016 -	12/2016	0(O) -	14/21
192	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	2,159.07	1,875.67	09/2008 -	03/2013	-	15/23
193	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATTISGARH	11/2012	11,846.00 -	11,846.00	1,321.00	05/2017 -	05/2017	0(O) -	8/37
194	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	1,527.00	64.00	08/2017 -	08/2017	0(O) -	0/8

Sector Wise Details

(March 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
195	MOUDA STPP - [N1800048]NTPC,MAHARASHTRA	11/2008	5,459.28 -	6,010.89	4,056.00	08/2012 -	03/2013	-	16/16
196	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	7,921.47	1,878.00	09/2016 -	09/2016	0(O) -	17/19
197	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	7,937.67	08/2013 -	06/2015	22(O) -	0/17
198	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL,MULTI STATE	02/2014	908.08 -	908.08	-	06/2016 -	06/2016	0(O) -	0/0
199	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 -	752.64	-	07/2013 -	03/2014	8(O) -	2/11
200	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	278.17	02/2012 -	12/2013	-	1/13
201	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	394.07	11/2011 -	-	-	2/14
202	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 -	539.82	-	06/2016 -	06/2016	0(O) -	0/0
203	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,007.98	04/2013 -	12/2014	20(O) -	0/11
204	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	314.55	11/2014 -	11/2014	0(O) -	2/12
205	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL,MULTI STATE	09/2013	680.69 -	680.69	-	03/2016 -	03/2016	0(O) -	0/0
206	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]PGCIL,MULTI STATE	09/2012	803.34 -	803.34	211.42	03/2015 -	03/2015	0(O) -	4/15
207	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	-	04/2015 -	05/2015	1(O) -	0/16
208	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	633.83	11/2012 -	04/2014	17(O) -	0/11
209	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,HIMACHAL PRADESH	10/2005	2,304.56 -	2,716.00	2,349.46	10/2010 -	08/2014	46(O) -	1/2
210	PARBATI HEP (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	5,366.00	4,373.85	09/2009 -	07/2018	106(O) -	0/12
211	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99 -	1,128.38	811.78	08/2013 09/2015	09/2015	25(O) 0(R)	17/26
212	RAMPUR HEP(412 MW) - [N18000024]SJVN,L,HIMACHAL PRADESH	01/2007	2,047.03 -	2,047.03	-	01/2012 -	-	-	19/28
213	RIHAND STTP STAGE-III (2X500MW) - [N18000073]NTPC,UTTAR PRADESH	01/2009	6,230.81 -	6,230.81	4,544.00	10/2012 -	10/2013	-	16/16
214	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	2,085.00	11/2016 -	11/2016	0(O) -	16/17
215	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]PGCIL,KARNATAKA	02/2014	167.40 -	167.40	-	12/2015 -	12/2015	0(O) -	0/0
216	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	10,667.00	6,788.54	09/2010 -	07/2018	94(O) -	0/0
217	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]PGCIL,MULTI STATE	08/2008	2,360.95 -	2,580.90	-	08/2012 -	03/2014	19(O) -	1/5
218	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,MULTI STATE	09/2012	1,508.74 -	1,508.74	247.12	06/2016 -	12/2015	-6(O) -	0/20

Sector Wise Details

(March 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
219	SYSTEM STRENGTHENING -XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	232.34	-	06/2012 -	-	-	0/3
220	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,MULTI STATE	09/2012	1,935.35 -	1,935.35	605.31	12/2014 -	11/2014	-1(O) -	2/2
221	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL,MADHYA PRADESH	03/2012	213.78 -	213.78	103.39	03/2014 -	06/2014	3(O) -	3/7
222	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 -	1,746.65	317.22	08/2014 -	05/2015	9(O) -	2/19
223	SYSTEM STRENGTHENING IN NR FOR SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	975.26	08/2012 -	12/2014	28(O) -	0/11
224	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]PGCIL,ANDHRA PRADESH	02/2014	243.53 -	243.53	-	08/2014 -	08/2014	0(O) -	0/0
225	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]PGCIL,MAHARASHTRA	02/2012	1,310.85 -	1,310.85	-	02/2015 -	02/2015	0(O) -	1/14
226	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,MULTI STATE	06/2012	1,263.26 -	1,263.26	598.85	11/2014 -	11/2014	0(O) -	0/16
227	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATISGARH	01/2012	1,422.85 -	1,422.85	633.79	01/2015 -	01/2015	0(O) -	4/19
228	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 -	297.33	214.02	08/2014 -	08/2014	0(O) -	7/20
229	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	487.49	277.05	06/2014 -	09/2014	3(O) -	8/20
230	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 -	3,846.30	2,020.00	03/2013 -	03/2017	48(O) -	0/13
231	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC, WEST BENGAL	09/2005	1,061.38 -	1,501.75	1,482.62	09/2009 -	07/2015	70(O) -	0/5
232	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,UTTAR PRADESH	07/2006	1,657.00 2,978.86	2,978.86	692.39	07/2010 02/2016	02/2017	79(O) 12(R)	1/10
233	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118]PGCIL,GUJARAT	01/2012	259.28 -	259.28	-	01/2014 -	-	-	3/15
234	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	963.76	08/2014 -	06/2015	10(O) -	2/19
235	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAND AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	1,427.54	10/2014 -	06/2015	8(O) -	3/18
236	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	3,739.68	10/2012 -	03/2015	29(O) -	0/11
237	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,MULTI STATE	02/2009	184.19 -	184.19	-	11/2011 -	-	-	0/4
238	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP & BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	1,647.80	12/2012 -	06/2015	30(O) -	0/11
239	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B - [N18000077]PGCIL, WEST BENGAL	04/2010	4,404.57 -	4,404.57	464.43	01/2015 -	12/2015	11(O) -	2/20

Sector Wise Details

(March 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
240	TRANSMISSION SYS ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1 - [N18000121]PGCIL,ANDHRA PRADESH	02/2012	324.33 -	324.33	141.27	08/2014 -	08/2014	0(O) -	9/20
241	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL,ANDHRA PRADESH	02/2012	1,927.16 -	1,927.16	906.91	10/2014 -	10/2014	0(O) -	3/16
242	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL,MULTI STATE	09/2013	1,575.30 -	1,575.30	-	05/2016 -	05/2016	0(O) -	0/0
243	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	393.96	02/2014 -	06/2014	4(O) -	5/17
244	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,MADHYA PRADESH	08/2011	425.51 -	425.51	-	10/2013 -	-	-	1/8
245	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]PGCIL,MULTI STATE	09/2011	1,366.34 -	1,366.34	952.26	12/2013 -	06/2014	6(O) -	4/13
246	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	241.16	11/2013 -	03/2015	16(O) -	7/20
247	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 -	2,074.86	-	03/2013 -	03/2014	12(O) -	5/15
248	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]PGCIL,MULTI STATE	03/2011	2,569.25 -	2,569.25	-	03/2014 -	03/2014	0(O) -	5/15
249	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19 -	2,743.19	-	12/2013 -	03/2014	3(O) -	2/8
250	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	66.52	01/2013 -	06/2015	29(O) -	5/18
251	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,182.61	11/2013 -	06/2015	19(O) -	5/16
252	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. - [N18000076]PGCIL,MULTI STATE	03/2010	4,672.99 -	4,672.99	2,964.78	11/2012 -	03/2015	28(O) -	0/15
253	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH	11/2011	2,127.51 -	2,127.51	-	07/2014 -	07/2014	0(O) -	3/14
254	TRIPURA GAS BASED POWER PROJECT - [N18000071]NNEPCO,TRIPURA	07/2009	421.01 623.44	951.48	745.55	07/2013 -	11/2014	16(O) -	18/25
255	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NNEPCO,MIZORAM	01/2011	913.63 -	913.63	573.22	07/2006 12/2015	12/2015	113(O) 0(R)	2/14
256	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	-	04/2016 -	04/2016	0(O) -	0/0
257	VINDHYACHAL STPP STAGE-V - [N18000134]NTPC,MADHYA PRADESH	12/2011	3,180.40 -	3,180.40	881.00	08/2015 -	08/2015	0(O) -	16/16
258	VINDHYACHAL STTP STAGE-IV - [N18000072]NTPC,MADHYA PRADESH	01/2009	5,915.00 -	5,915.00	3,401.00	10/2012 -	03/2013	-	15/15
259	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,UTTARAKHAND	08/2008	2,491.58 -	3,745.08	479.33	07/2014 -	07/2018	48(O) -	1/1

Sector Wise Details

(March 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
260	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 -	477.69	471.52	09/2010 -	06/2014	45(O) -	0/5
261	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATISGARH	03/2012	9,569.76 -	9,569.76	1,577.68	06/2015 -	12/2015	6(O) -	3/28
	Total		244,469.88 -	263,493.12	114,382.25				385/1273
	<u>RAILWAYS</u>								
262	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	182.06 -	184.06	2.19	- -	-	-	0/0
263	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,TRIPURA	04/2008	813.34 813.34	1,141.75	545.80	03/2014 -	03/2017	36(O) -	0/0
264	AGARTALA-AKHAURA NL - [N22000195]NEFR,TRIPURA	04/2012	252.00 -	252.00	-	- -	-	-	0/0
265	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	432.72	399.71	12/2009 03/2011	03/2014	51(O) 36(R)	0/0
266	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	567.18	2.00	- -	-	-	0/0
267	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	385.60	55.12	03/2013 -	03/2013	-	0/0
268	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	353.08 514.68	2,820.00	307.10	- -	-	-	0/0
269	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	218.39	19.44	- -	-	-	0/0
270	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	822.00	-	- -	-	-	0/0
271	AKKANAPET-MEDAK - [N22000285](SCR),ANDHRA PRADESH	04/2012	153.00 -	153.00	-	- -	-	-	0/0
272	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263](SCR),MULTI STATE	04/2008	184.26 -	2,000.00	25.90	- -	-	-	0/0
273	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,MULTI STATE	12/2006	170.00 170.00	485.00	417.49	03/2011 03/2011	03/2011	-	0/0
274	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	242.09	-	- -	-	-	0/0
275	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	338.54	104.65	- -	-	-	0/0
276	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NEFR,ASSAM	04/2011	312.12 -	312.12	76.43	- -	03/2016	-	0/0
277	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	120.90 663.01	725.00	571.31	06/1999 03/2011	03/2011	-	0/0
278	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	295.68	0.68	- -	-	-	0/0
279	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	307.00	-	- -	-	-	0/0
280	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	1,566.00	137.40	- -	-	-	0/0
281	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	490.80	0.39	- -	-	-	0/0

Sector Wise Details

(March 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
282	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	304.41	0.19	- -	-	-	0/0
283	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	528.00	2.95	- -	-	-	0/0
284	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	160.89 199.75	199.75	45.46	- -	-	-	0/0
285	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	986.30	37.58	- -	-	-	0/0
286	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	288.35	5.96	- -	-	-	0/0
287	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 207.52	207.52	191.41	12/2012 -	12/2014	24(O) -	0/0
288	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	02/1999	138.00 901.62	901.62	5.35	- -	-	-	0/0
289	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	246.08	1.28	- -	-	-	0/0
290	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,WEST BENGAL	03/1998	111.90 1,039.29	1,423.98	478.50	03/2005 12/2008	12/2016	141(O) 96(R)	0/0
291	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	245.15 1,106.62	1,106.62	231.66	12/2010 03/2011	03/2011	-	0/0
292	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	450.55	10.88	- -	-	-	0/0
293	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	255.64	-	- -	-	-	0/0
294	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	401.81 495.44	1,814.10	369.57	03/2004 12/2010	12/2014	129(O) 48(R)	0/0
295	BHADRACHALAM ROAD-SATTUPALLI - [N22000287](SCR),ANDHRA PRADESH	04/2010	337.49 -	337.49	0.21	- -	-	-	0/0
296	BHADRACHALAM-KOVVUR - [N22000264](SCR),ANDHRA PRADESH	04/2012	923.23 -	923.23	-	- -	-	-	0/0
297	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	289.64	0.09	- -	-	-	0/0
298	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,MIZORAM	04/2008	619.34 -	2,393.48	171.49	04/2014 -	03/2017	35(O) -	0/0
299	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	2,966.99	40.79	- -	-	-	0/0
300	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	196.95	194.41	03/2011 -	-	-	0/0
301	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	195.64	79.94	- -	-	-	0/0
302	BHOPAL BINA 3D LINE DOUBLING - [N22000077]JRVNL,MADHYA PRADESH	09/2007	687.20 -	800.00	-	03/2010 -	12/2015	69(O) -	0/0
303	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	484.61	2.07	03/2012 -	-	-	0/0
304	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	326.20	1.67	- -	-	-	0/0
305	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	175.80	1.12	- -	-	-	0/0

Sector Wise Details

(March 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
306	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	267.37	34.01	- -	-	-	0/0
307	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]NEFR,ASSAM	09/1997	1,000.00 1,500.00	4,500.00	3,092.23	04/2008 03/2014	12/2017	116(O) 45(R)	0/0
308	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	579.37	599.40	- -	02/2012	-	0/0
309	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	177.38	54.89	03/2015 -	12/2015	9(O) -	0/0
310	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	328.14	0.18	- -	-	-	0/0
311	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	337.96	60.00	- -	-	-	0/0
312	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00 -	951.24	540.50	- -	12/2014	- -	0/0
313	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	222.95	112.40	- -	-	-	0/0
314	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1999	271.24 -	520.00	461.30	- -	-	-	0/0
315	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	1,200.00	2.03	- -	-	-	0/0
316	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 295.00	494.92	0.32	- -	-	-	0/0
317	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]JECOR,BIHAR	04/2006	285.07 -	378.56	103.76	- -	-	-	0/0
318	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,BIHAR	03/2005	470.09 1,417.97	1,417.97	1,011.09	- -	03/2012	-	0/0
319	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	585.93	194.91	- -	12/2013	-	0/0
320	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	243.78	27.13	- -	-	-	0/0
321	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	327.25	-	- -	-	-	0/0
322	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	558.00	-	- -	-	-	0/0
323	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	595.91	89.53	- -	-	-	0/0
324	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	1,347.26	145.75	- -	-	-	0/0
325	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP,WEST BENGAL	04/2009	573.78 -	573.78	166.84	- -	-	-	0/0
326	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR - [N22000083]NEFR,ARUNACHAL PRADESH	09/1996	156.00 156.00	406.40	406.33	- -	03/2014	- -	0/0
327	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NEFR,TRIPURA	04/1999	895.00 -	1,091.98	955.94	03/2007 -	03/2017	120(O) -	0/0
328	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	556.64	266.66	- -	-	-	0/0

Sector Wise Details									
(March 2014)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
329	CUMBUM-PRODDATUR - [N22000282](SCR),ANDHRA PRADESH	04/2013	829.00 -	829.00	-	- -	-	-	0/0
330	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	1,640.04	160.91	- -	-	-	0/0
331	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	259.51 533.38	533.38	105.32	12/2011 02/2012	02/2012	-	0/0
332	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	968.60	-	12/2012 -	-	-	0/0
333	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	388.67	74.58	12/2015 -	12/2015	0(O) -	0/0
334	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	104.79 -	406.92	145.42	- -	-	-	0/0
335	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	296.44	3.86	- -	-	-	0/0
336	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	366.73 -	366.73	4.95	- -	-	-	0/0
337	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	151.84 410.08	410.08	242.95	- -	03/2014	- -	0/0
338	DELHI-SOHA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	1,239.00	-	- -	-	-	0/0
339	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	336.91	142.83	- -	-	-	0/0
340	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	138.00 607.09	607.09	533.29	12/2012 12/2012	02/2013	-	0/0
341	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	376.59	2.00	- -	-	-	0/0
342	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 2,030.50	2,030.50	1.60	02/2019 -	02/2019	0(O) -	0/0
343	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SWR,MULTI STATE	04/2010	553.63 -	651.17	7.08	- -	-	-	0/0
344	DIMAPUR-TIZIT NL - [N22000196]NEFR,NAGALAND	04/2013	4,274.00 -	4,274.00	-	- -	-	-	0/0
345	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 343.17	914.98	744.56	- -	12/2012	-	0/0
346	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	4,874.58	-	03/2016 -	03/2016	0(O) -	0/0
347	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 224.89	246.44	141.55	03/2012 12/2013	03/2014	24(O) 3(R)	0/0
348	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	189.24	2.09	- -	-	-	0/0
349	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	603.22	1.49	- -	-	-	0/0
350	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	09/2001	120.00 245.39	245.39	225.46	12/2008 -	09/2014	69(O) -	0/0
351	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	495.74	264.06	06/2013 06/2013	03/2015	21(O) 21(R)	0/0

Sector Wise Details

(March 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
352	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	654.00	-	- -	-	-	0/0
353	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,MULTI STATE	03/1984	520.00 835.04	835.04	622.92	03/1995 -	03/2015	240(O) -	0/0
354	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	1,117.00	-	- -	-	-	0/0
355	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	270.00	293.11	02/2011 02/2011	03/2013	-	0/0
356	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	415.67	13.88	- -	-	-	0/0
357	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	445.25	1.14	- -	-	-	0/0
358	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	189.97 -	611.03	136.27	12/2011 11/2013	11/2013	-	0/0
359	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	186.92 261.70	261.70	72.78	02/2006 -	06/2015	112(O) -	0/0
360	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,UTTAR PRADESH	03/2002	381.17 863.23	863.23	787.13	- -	03/2012	-	0/0
361	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,038.00	1,038.00	590.26	03/1998 -	-	-	0/0
362	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	159.20 -	156.65	53.64	- -	-	-	0/0
363	GUDUR-DURGARA JAPATNAM - [N22000265](SCR),ANDHRA PRADESH	04/2011	283.54 -	283.54	0.16	- -	-	-	0/0
364	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	832.00	402.47	- 05/2009	05/2009	-	0/0
365	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	608.02	583.67	03/1994 -	01/2014	-	0/0
366	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	206.22	8.17	- -	-	-	0/0
367	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 3,845.60	3,845.60	1.92	02/2020 -	02/2020	0(O) -	0/0
368	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	157.17	76.39	- -	-	-	0/0
369	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	213.01	-	- -	-	-	0/0
370	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	324.66 528.65	528.65	195.19	- -	-	-	0/0
371	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	267.09	0.91	- -	-	-	0/0
372	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	172.03	5.05	- -	-	-	0/0
373	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	1,185.64	-	- 09/2009	-	-	0/0
374	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	329.97	-	- -	-	-	0/0
375	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N22000052]WS&PU,BIHAR	04/2003	98.74 224.51	337.30	222.07	- -	03/2012	-	0/0
376	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 412.91	412.91	872.87	- -	01/2013	-	0/0

Sector Wise Details

(March 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
377	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 230.03	230.03	151.26	- -	03/2014	- -	0/0
378	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 829.74	829.74	53.05	03/2015 -	03/2015	0(O) -	0/0
379	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	400.00	-	- -	-	-	0/0
380	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	2,127.00	46.57	- -	-	-	0/0
381	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	157.94	41.57	- -	-	-	0/0
382	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]RE, WEST BENGAL	04/1974	31.42 393.46	445.40	179.36	03/2007 03/2007	03/2015	96(O) 96(R)	0/0
383	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	166.89	0.02	- -	-	-	0/0
384	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	2,135.00	110.08	- -	-	-	0/0
385	HYDERABAD/SECUNDERABD MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II - [N22000213]MRTP,ANDHRA PRADESH	04/2012	632.68 -	816.55	17.37	04/2012 -	03/2016	47(O) -	0/0
386	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,ANDHRA PRADESH	04/2007	313.24 -	313.24	176.96	01/1999 -	-	-	0/0
387	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 653.19	653.47	277.38	03/2014 -	03/2014	0(O) -	0/0
388	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	165.65 -	165.65	141.36	- -	-	-	0/0
389	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	409.00 625.30	847.75	837.70	06/2007 -	06/2007	-	0/0
390	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	233.00 501.69	1,043.56	732.63	03/2012 08/2012	-	-	0/0
391	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	470.00	59.44	- -	-	-	0/0
392	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	190.81 238.56	740.00	544.86	03/2012 03/2012	12/2012	-	0/0
393	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,MANIPUR	04/2003	727.56 727.53	4,478.17	2,023.83	03/2011 03/2014	03/2017	72(O) 36(R)	0/0
394	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288](SCR),MULTI STATE	04/2008	2,050.00 -	2,050.00	92.33	- -	-	-	0/0
395	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	923.52	236.31	- -	-	-	0/0
396	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	174.56	55.00	- -	-	-	0/0
397	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	279.70	3.51	- -	-	-	0/0
398	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,UTTAR PRADESH	03/1997	395.00 1,577.45	1,708.41	1,549.78	- -	03/2013	-	0/0

Sector Wise Details

(March 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
399	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	643.00	-	- -	-	-	0/0
400	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	323.40 744.71	744.71	521.04	- -	03/2014	-	1/1
401	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 155.00	800.00	773.42	- -	10/2012	-	0/0
402	KATAKHAL TO BHAIRABI - [N22000126]NEFR,ASSAM	04/1998	227.90 227.90	218.36	133.58	12/2012 -	03/2018	63(O) -	0/0
403	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,BIHAR	09/2001	100.00 492.98	725.53	445.01	12/2010 12/2010	03/2015	51(O) 51(R)	0/0
404	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66 -	423.66	158.41	03/2017 -	03/2017	0(O) -	0/0
405	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261](SCR),MULTI STATE	04/2012	1,054.35 -	1,054.35	0.42	- -	-	-	0/0
406	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	78.23 162.87	162.87	126.82	- -	-	-	0/0
407	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	276.00	-	03/2009 03/2009	08/2014	65(O) 65(R)	0/0
408	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	355.38 470.21	1,995.25	295.81	- -	12/2014	-	0/0
409	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,BIHAR	04/2008	282.92 282.92	359.86	2.22	- -	03/2015	-	0/0
410	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	371.36 768.87	768.87	539.61	- 03/2010	03/2010	-	0/0
411	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	491.19 2,957.21	2,957.21	1,745.01	07/2005 -	-	-	0/0
412	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 418.17	418.17	217.86	- -	-	-	0/0
413	KONDAPALLI-PENUBALLI - [N22000260](SCR),ANDHRA PRADESH	04/2013	723.00 -	723.00	-	- -	-	-	0/0
414	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	323.41 322.95	341.41	295.38	03/2012 03/2013	03/2013	-	0/0
415	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 1,047.00	1,045.20	9.41	- -	-	-	0/0
416	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	252.96	1.52	- -	-	-	0/0
417	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	192.56	0.38	- -	-	-	0/0
418	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	346.15	14.61	- -	-	-	0/0
419	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1999	406.99 -	406.99	142.79	- -	-	-	0/0
420	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,MULTI STATE	09/1998	925.00 -	1,630.97	488.13	05/2008 03/2011	-	-	0/0
421	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	257.42	34.36	03/2014 -	03/2014	0(O) -	0/0

Sector Wise Details									
(March 2014)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
422	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NEFR,ASSAM	04/2012	246.07 -	246.07	1.11	- -	-	-	0/0
423	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NEFR,ASSAM	04/1996	1,676.31 1,676.31	4,184.84	4,020.98	03/2009 -	03/2017	96(O) -	0/0
424	MACHERLA-NALGONDA(NL)-(SCR) - [220100220]SCR,ANDHRA PRADESH	07/1998	125.00 -	480.00	0.86	07/2008 -	07/2008	-	0/0
425	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	450.00	12.39	- -	-	-	0/0
426	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	800.00	0.48	- -	-	-	0/0
427	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRATH-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	493.96	117.82	- -	-	-	0/0
428	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 218.19	472.00	192.27	- -	02/2013	-	0/0
429	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	184.00 900.05	900.05	794.42	12/2011 12/2011	03/2013	-	0/0
430	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,ANDHRA PRADESH	04/2006	378.56 671.82	791.59	0.76	- -	-	-	0/0
431	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 -	258.20	1.18	- -	03/2016	-	0/0
432	MANSABHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	396.04	88.77	- -	-	-	0/0
433	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	114.01 332.92	477.88	451.33	03/2012 03/2013	03/2013	-	0/0
434	MANUGURU-RAMAGUNDAM - [N22000259](SCR),ANDHRA PRADESH	04/2013	1,112.00 -	1,112.00	-	- -	-	-	0/0
435	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	285.57	1.07	01/1999 -	-	-	0/0
436	MAVLI JN.-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	965.16	558.00	- -	-	-	0/0
437	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 404.19	1,383.45	396.53	- -	-	-	0/0
438	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	289.79 -	377.44	0.33	- -	-	-	0/0
439	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WJR,GUJARAT	04/2011	439.88 -	439.88	0.70	- -	-	-	0/0
440	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	466.48	0.25	01/1999 -	-	-	0/0
441	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	276.69	-	01/1999 -	-	-	0/0
442	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	250.93	-	- -	-	-	0/0
443	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	211.00	4.41	- -	-	-	0/0
444	MUDKHED-PARBHANI - [N22000283](SCR),MAHARASHTRA	04/2011	390.60 -	390.60	1.85	- -	-	-	0/0

Sector Wise Details

(March 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
445	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 5,300.00	6,213.84	1,509.46	03/2014 03/2016	12/2016	33(O) 9(R)	0/0
446	MUNEERABAD-MAHABOBNAGAR(NL), SCR - [N220100205]SCR, MULTI STATE	04/1997	218.24 377.32	645.00	225.04	- -	03/2014	- -	0/0
447	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR, KARNATAKA	04/2007	179.65 -	1,350.91	256.61	- -	-	-	0/0
448	MURKONGSELEK-PASIGHAT NL - [N22000208]NEFR, MULTI STATE	04/2011	165.82 -	165.82	38.65	- -	-	-	0/0
449	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR, BIHAR	04/2008	281.30 -	281.30	0.58	- -	-	-	0/0
450	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR, BIHAR	04/2008	228.05 -	228.05	1.47	- -	-	-	0/0
451	NABADWIPDHAM-PATULI DOUBLING - [N22000246]ER, MULTI STATE	04/2010	169.82 -	169.82	32.10	- -	-	-	0/0
452	NADIKUDE-SRI KALAHASTI - [N22000286](SCR), ANDHRA PRADESH	04/2011	1,313.48 -	1,313.48	0.64	- -	-	-	0/0
453	NANDYAL-YERRAGUNTALA(NL), SCR - [N220100192]SCR, ANDHRA PRADESH	03/1996	155.74 429.49	883.00	679.45	02/2009 -	03/2012	-	0/0
454	NANGALDAM-TALWARA(NL), NR - [N220100188]NR, MULTI STATE	03/1981	37.68 450.00	1,036.78	383.89	07/2012 -	-	-	0/0
455	NAWADA-LAXMIPUR (NL) - [N22000167]SER, BIHAR	04/2008	620.57 -	620.57	-	- -	-	-	0/0
456	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER, MULTI STATE	04/2010	494.54 -	494.54	31.92	- -	-	-	0/0
457	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NEFR, BIHAR	09/2006	300.00 300.00	532.87	43.94	- -	-	-	0/0
458	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NEFR, ASSAM	09/2006	200.00 200.00	385.20	181.12	- -	03/2018	- -	0/0
459	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NEFR, MULTI STATE	04/2010	242.22 -	242.22	39.67	- -	-	-	0/0
460	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NEFR, MEGHALAYA	04/2010	4,083.02 -	4,083.02	3.37	- -	-	-	0/0
461	NEW BG LINE FROM DUDHNOI-MENDIPATAR - [N22000192]NEFR, MULTI STATE	04/1999	175.43 -	175.43	220.68	- -	03/2014	- -	0/0
462	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NEFR, MULTI STATE	04/2010	241.52 -	241.52	148.33	- -	03/2016	- -	0/0
463	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NEFR, WEST BENGAL	04/2010	221.42 -	222.21	21.89	- -	-	-	0/0
464	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR - [N220100135]NEFR, WEST BENGAL	04/1983	36.80 274.41	703.17	252.52	- -	03/2015	- -	0/0
465	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NEFR, MULTI STATE	04/2013	1,798.00 -	1,798.00	-	- -	-	-	0/0
466	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NEFR, WEST BENGAL	04/2011	209.77 -	209.77	34.24	- -	03/2017	- -	0/0
467	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NEFR, WEST BENGAL	04/2012	283.55 -	283.55	1.14	- -	03/2017	- -	0/0

Sector Wise Details

(March 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
468	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NEFR,MULTI STATE	04/1999	523.17 -	1,327.78	947.86	- -	-	-	0/0
469	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NEFR,NAGALAND	04/2006	850.00 850.00	850.00	9.24	03/2015 -	03/2017	24(O) -	0/0
470	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NEFR,MULTI STATE	04/2000	733.00 733.00	1,655.81	1,552.32	12/2008 -	03/2018	111(O) -	0/0
471	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,298.42	64.57	03/2014 -	03/2016	24(O) -	0/0
472	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,619.02 -	2,913.51	398.86	03/2016 -	03/2016	0(O) -	0/0
473	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	78.35	03/2016 -	06/2016	3(O) -	0/0
474	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	3,951.98	308.18	03/2016 -	03/2016	0(O) -	0/0
475	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, ANDHRA PRADESH	07/2006	743.00 -	1,117.11	-	03/2008 06/2008	-	-	0/0
476	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR, GUJARAT	04/2013	1,266.89 -	1,266.89	-	- -	-	-	0/0
477	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	225.68 293.74	293.74	139.49	12/2010 12/2010	12/2010	-	0/0
478	PANVEL PEN DOUBLING - [N22000255]CR, MULTI STATE	04/2006	191.00 -	260.16	217.77	- -	05/2014	-	0/0
479	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR, BIHAR	04/2001	624.47 2,921.00	2,921.00	2,071.46	10/2007 12/2012	12/2015	98(O) 36(R)	0/0
480	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, ANDHRA PRADESH	12/1994	124.43 495.68	925.30	663.66	- -	02/2014	-	0/0
481	PEN ROHA DOUBLING - [N22000254]CR, MULTI STATE	04/2007	203.00 -	203.00	177.40	- -	03/2014	-	0/0
482	PIRPAINTI-BHAGALPUR - [N22000222]ER, MULTI STATE	04/2011	261.38 -	261.38	18.50	- -	-	-	0/0
483	PIRPAINTI-JASIDIH - [N22000219]ER, MULTI STATE	04/2013	915.98 -	915.98	0.09	- -	-	-	0/0
484	PLASSEY-JAGANJ DOUBLING - [N22000220]ER, MULTI STATE	04/2011	248.07 -	248.07	12.05	03/2015 -	03/2015	0(O) -	0/0
485	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER, MULTI STATE	04/2011	299.60 -	299.60	1.10	03/2017 -	03/2017	0(O) -	0/0
486	PUSHKAR-MERTA - [N22000151]NWR, RAJASTHAN	04/2013	323.00 -	323.00	-	- -	-	-	0/0
487	QADIAN-BEAS - [N22000295]NR, PUNJAB	04/2011	205.22 -	205.22	1.54	- -	-	-	0/0
488	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR, TAMIL NADU	04/1999	460.94 -	1,030.00	800.90	01/1999 -	-	-	0/0

Sector Wise Details

(March 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
489	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE	03/1998	280.00 -	1,122.00	834.61	- -	03/2013	-	0/6
490	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	289.93	-	12/2007 03/2010	-	-	0/0
491	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 2,363.00	2,363.00	1,339.96	03/2009 12/2012	12/2014	69(O) 24(R)	0/0
492	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	288.00	-	02/2009 02/2009	08/2014	66(O) 66(R)	0/0
493	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 -	913.48	461.85	- -	-	-	0/0
494	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 482.70	482.70	560.17	03/2013 -	03/2014	12(O) -	0/0
495	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	727.13 727.13	1,225.90	238.15	- -	-	-	0/0
496	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 194.07	596.36	371.50	06/2004 -	12/2014	126(O) -	0/0
497	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]NEFR,MULTI STATE	01/2004	915.70 915.70	2,232.50	2,664.89	- -	03/2015	- -	0/0
498	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	288.97	-	- -	-	-	0/0
499	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	872.22	787.83	- -	-	-	0/0
500	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2012	2,082.75 -	2,082.75	21.64	- -	-	-	0/0
501	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	1,421.25	344.42	03/2012 -	-	-	0/0
502	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	970.34	266.76	- -	-	-	0/0
503	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	755.54	8.50	- -	-	-	0/0
504	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	714.10	18.16	- 12/2017	12/2017	- 0(R)	0/0
505	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	193.44	14.67	- -	-	-	0/0
506	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	325.00	240.38	- -	-	-	0/0
507	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	355.81	338.97	- -	-	-	0/0
508	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	385.54	-	03/2010 -	-	-	0/0
509	SANTOSH PUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	268.52	78.85	- -	-	-	0/0
510	SEVOK RANGPO, NEFR - [N22000102]NEFR,SIKKIM	04/2008	1,339.48 -	3,380.58	82.93	12/2015 -	03/2017	15(O) -	0/0
511	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	562.74	1.06	- -	-	-	0/0

Sector Wise Details									
(March 2014)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
512	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	678.62	16.35	- -	-	-	0/0
513	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	297.47	51.81	- -	-	-	0/0
514	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	277.28	42.61	- -	-	-	0/0
515	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	296.00	-	- -	-	-	0/0
516	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	839.00	0.01	- -	-	-	0/0
517	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	818.29	111.78	02/2015 -	02/2015	0(O) -	0/0
518	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	450.00	8.02	- -	-	-	0/0
519	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 516.23	516.23	478.66	03/2014 -	03/2014	0(O) -	0/0
520	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	726.96 810.78	810.78	133.24	- -	-	-	0/0
521	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 1,013.74	1,074.45	457.52	06/2005 07/2011	06/2016	132(O) 59(R)	0/0
522	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	146.95 -	171.02	141.84	06/2013 -	06/2014	12(O) -	0/0
523	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	365.17	1.39	- -	-	-	0/0
524	TARAKESHWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	157.96 1,188.91	1,188.91	665.23	- 12/2009	02/2012	-	0/0
525	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	236.93	0.03	- -	-	-	0/0
526	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 456.00	820.00	185.24	- -	-	-	0/0
527	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 125.00	420.00	60.46	- -	-	-	0/0
528	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	167.73	80.37	03/2012 -	02/2013	-	0/0
529	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 100.00	900.00	566.35	- -	-	-	0/0
530	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL	03/2000	907.69 3,156.32	3,176.10	3,485.95	12/2006 08/2010	08/2010	-	0/0
531	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	1,801.01	1.26	- -	-	-	0/0
532	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 2,500.00	20,000.00	8,822.50	11/2002 -	12/2017	181(O) -	0/0
533	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	1,389.62	796.60	03/2014 -	03/2014	0(O) -	0/0
534	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	380.00	1.10	- -	-	-	0/0

Sector Wise Details

(March 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
535	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 325.00	1,116.53	277.91	03/2010 03/2017	03/2017	84(O) 0(R)	0/0
536	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	1,280.83	0.84	- -	-	-	0/0
537	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 -	548.01	200.15	- 03/2010	-	-	0/0
538	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	685.17	105.30	- -	-	-	0/0
539	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	279.40	188.74	- -	04/2014	- -	0/0
540	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	697.00 -	2,501.05	66.64	- -	-	-	0/0
541	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	297.85	3.90	- -	-	-	0/0
542	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	348.85	1.04	- -	-	-	0/0
543	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	876.00	-	- -	-	-	0/0
	Total		148,551.55 -	257,231.72	77,727.25				1/7
	ROAD TRANSPORT AND HIGHWAYS								
544	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	333.05	08/2013 -	-	-	0/0
545	2 LANING OF MUZAFFARPUR - SONBARSA - [N24000174]NHAI,BIHAR	05/2011	511.54 -	511.54	65.78	11/2013 -	11/2013	-	0/0
546	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH	10/2012	250.50 -	250.50	328.56	10/2014 -	10/2014	0(O) -	0/0
547	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	373.47	43.77	07/2014 -	07/2014	0(O) -	0/0
548	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	351.54	394.67	05/2013 -	-	-	0/0
549	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	687.49	11/2013 -	-	-	0/0
550	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	624.00	424.10	04/2014 -	04/2014	0(O) -	0/0
551	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]NHAI,MADHYA PRADESH	10/2011	1,565.00 -	1,565.00	1,119.27	10/2014 -	10/2014	0(O) -	0/0
552	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	356.40	42.51	07/2014 -	07/2014	0(O) -	0/0
553	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	119.17	01/2014 -	01/2014	-	0/0
554	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	226.00	332.50	02/2014 -	02/2014	-	0/0
555	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	664.00	688.13	02/2014 -	02/2014	-	0/0
556	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	174.34	04/2014 -	04/2014	0(O) -	0/0

Sector Wise Details

(March 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
557	2LANING WITH PS GOPALGANJ-CHAPRA - [N24000190]NHAI,BIHAR	12/2011	325.00 -	325.00	166.73	05/2014 -	05/2014	0(0) -	0/0
558	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT	03/2012	828.00 -	828.00	582.60	09/2014 -	09/2014	0(0) -	0/3
559	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	2,425.10	08/2014 -	08/2014	0(0) -	0/0
560	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT	12/2010	1,008.50 -	1,008.50	1,356.04	06/2013 -	-	-	0/3
561	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	39.49	09/2013 -	07/2014	10(0) -	0/0
562	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,GUJARAT	03/2011	785.50 -	785.50	848.81	08/2013 -	-	-	0/3
563	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	398.00	457.03	02/2014 -	02/2014	-	0/0
564	4-LANING OF BRAHAMPURE-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	998.79	1,486.08	08/2013 -	-	-	0/0
565	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	1,078.84	1,469.16	08/2013 -	-	-	0/0
566	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	580.43	305.67	08/2013 -	-	-	0/0
567	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	819.07	07/2013 -	-	-	0/0
568	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	1,396.18	1,383.05	09/2014 -	09/2014	0(0) -	0/0
569	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 385.15	385.15	269.40	09/2007 07/2011	-	-	0/0
570	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	2,125.24	61.44	12/2015 -	12/2015	0(0) -	0/3
571	AMRITSAR-PATHANKOT - [N24000147]NHAI,PUNJAB	05/2010	705.00 -	705.00	2,182.60	11/2012 -	-	-	0/0
572	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,ANDHRA PRADESH	02/2010	390.56 -	390.56	772.40	02/2012 -	06/2013	-	0/0
573	BAREILY-SITAPUR - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	366.40	09/2013 -	-	-	0/0
574	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	867.00	598.56	02/2015 -	02/2015	0(0) -	0/0
575	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	2,388.00	1,846.87	06/2014 -	06/2014	0(0) -	0/0
576	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,KARNATAKA	12/2010	480.00 -	480.00	649.04	- -	-	-	2/2
577	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	209.00	38.26	01/2013 -	-	-	0/0
578	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	500.29	579.27	08/2013 -	-	-	0/0
579	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	237.80	292.51	06/2008 -	-	-	0/0
580	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	195.00	262.98	06/2008 -	-	-	0/0
581	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	230.00	240.09	06/2005 -	-	-	0/0

Sector Wise Details

(March 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
582	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	309.56	306.32	04/2010 01/2016	01/2016	69(O) 0(R)	0/0
583	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	281.31	180.06	02/2010 -	-	-	0/0
584	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	864.53	03/2013 -	-	-	0/0
585	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	353.37	446.24	10/2011 -	-	-	0/0
586	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	572.30	886.91	10/2011 -	-	-	0/0
587	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,KARNATAKA	03/2011	839.00 -	839.00	684.71	- -	-	-	0/1
588	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	957.80	05/2013 -	-	-	0/0
589	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	300.00	181.32	10/2008 -	-	-	0/0
590	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	1,928.22	428.98	04/2015 -	04/2015	0(O) -	0/0
591	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	661.58	05/2010 -	03/2014	46(O) -	0/0
592	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	593.00	685.53	07/2013 -	-	-	0/0
593	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	312.85	06/2013 -	-	-	0/0
594	DEVIHALLI-HASSAN - [N24000152]NHAI,KARNATAKA	12/2010	453.00 -	453.00	761.25	- -	-	-	1/1
595	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	200.00	257.33	06/2008 -	-	-	0/0
596	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	209.92	05/2008 07/2014	07/2014	74(O) 0(R)	0/0
597	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	232.45	308.97	09/2010 -	-	-	0/0
598	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	1,573.00	37.66	09/2015 -	09/2015	0(O) -	0/0
599	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	332.94	511.54	09/2008 -	-	-	0/0
600	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00 -	1,232.00	252.60	08/2015 -	08/2015	0(O) -	0/0
601	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	682.00	307.91	10/2013 -	03/2014	5(O) -	0/0
602	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	201.66	150.62	09/2008 -	-	-	0/0
603	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 1,141.00	1,141.00	1,319.54	08/2013 06/2014	06/2014	10(O) 0(R)	0/0
604	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	1,509.10	2,021.74	09/2012 -	-	-	2/3
605	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	198.16	306.31	04/2008 01/2015	01/2015	81(O) 0(R)	0/0
606	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	175.96	249.37	04/2008 01/2015	01/2015	81(O) 0(R)	0/0

Sector Wise Details

(March 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
607	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	495.40	12/2009 -	-	-	0/0
608	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 361.00	361.00	339.45	02/2009 -	05/2014	63(O) -	0/0
609	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 331.23	331.23	183.67	07/2009 -	04/2014	57(O) -	0/0
610	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 333.83	333.83	73.71	09/2007 -	05/2014	80(O) -	0/0
611	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	478.00	308.92	10/2013 -	03/2014	5(O) -	0/0
612	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	625.07	995.85	01/2013 -	-	-	0/0
613	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	946.00	1,077.27	- -	-	-	3/3
614	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	325.00	574.80	05/2013 -	-	-	0/0
615	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	-	-	0/0
616	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	267.81	685.86	02/2013 -	-	-	0/0
617	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	792.06	1,980.90	12/2012 -	-	-	0/0
618	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	999.79	07/2013 -	-	-	0/0
619	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	574.50	01/2014 -	01/2014	-	0/0
620	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	711.11	07/2013 -	-	-	0/0
621	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	795.00	1,128.18	05/2012 -	-	-	0/0
622	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	250.39	283.31	10/2008 -	-	-	0/0
623	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	651.04	07/2014 -	07/2014	0(O) -	0/0
624	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,KARNATAKA	09/2010	671.00 -	671.00	938.40	- -	06/2014	- -	2/3
625	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	635.90	459.85	07/2012 -	-	-	0/0
626	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 241.28	241.28	151.77	11/2008 12/2014	12/2014	73(O) 0(R)	0/0
627	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 382.02	382.02	107.55	04/2009 12/2014	12/2014	68(O) 0(R)	0/0
628	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 265.53	265.63	92.14	11/2008 12/2014	12/2014	73(O) 0(R)	0/0
629	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 247.43	247.43	180.36	04/2009 12/2014	12/2014	68(O) 0(R)	0/0
630	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,122.23	06/2013 -	-	-	0/0
631	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	517.00	03/2013 -	-	-	0/0

Sector Wise Details									
(March 2014)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
632	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	264.72	303.05	06/2008 -	-	-	0/0
633	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19 -	484.19	283.53	10/2014 -	10/2014	0(O) -	0/0
634	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	208.00	313.93	04/2008 01/2015	01/2015	81(O) 0(R)	0/0
635	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	269.79	06/2008 05/2014	05/2014	71(O) 0(R)	0/0
636	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	200.00	308.16	06/2008 -	-	-	0/0
637	NASHRI CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	06/2010	2,159.00 -	2,159.00	374.22	06/2015 -	06/2015	0(O) -	0/0
638	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	1,655.00	524.67	09/2013 -	-	-	0/0
639	NH CONNECTIVITY TO ICTT VALLARPADAUE NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	557.00	1,129.29	02/2010 -	-	-	0/0
640	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	586.00	237.60	01/2014 -	01/2014	-	0/0
641	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	158.91	09/2014 -	09/2014	0(O) -	0/0
642	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	-	-	0/0
643	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00 -	807.00	1,325.75	10/2014 -	10/2014	0(O) -	0/0
644	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	942.69	264.53	06/2014 -	06/2014	0(O) -	0/0
645	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	574.00	794.16	03/2014 -	03/2014	0(O) -	0/0
646	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	630.90	02/2013 -	-	-	0/0
647	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	940.00	1,339.69	07/2012 -	-	-	0/0
648	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,206.67	03/2013 -	-	-	0/0
649	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	835.00	425.19	01/2014 -	01/2014	-	0/0
650	PUNE-SHOLAPUR,PKG1 - [N24000127]NHAI,MAHARASHTRA	11/2009	1,110.00 -	1,110.00	1,825.57	05/2012 -	-	-	0/0
651	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,080.00	07/2015 -	07/2015	0(O) -	0/0
652	RAJMARG CHORHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHA) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	251.03	351.82	10/2008 -	-	-	0/0
653	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,MULTI STATE	12/2012	1,479.00 -	1,479.00	285.46	06/2015 -	06/2015	0(O) -	0/0
654	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN	03/2012	333.51 -	333.51	260.16	09/2014 -	09/2014	0(O) -	0/0
655	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	650.00	1,160.37	11/2013 -	01/2014	-	0/0
656	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	805.39	765.39	03/2013 -	-	-	0/0

Sector Wise Details									
(March 2014)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
657	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	909.00	959.15	05/2014 -	05/2014	0(O) -	0/0
658	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 157.47	157.47	260.30	09/2007 03/2014	12/2013	-	0/0
659	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	225.00	191.72	07/2008 -	-	-	0/0
660	SIX LANNING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	1,047.00	234.03	06/2014 -	06/2014	0(O) -	0/0
661	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	535.00	52.18	12/2013 -	12/2013	-	0/0
662	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,169.28	12/2013 -	12/2013	-	0/0
663	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	1,328.51	05/2014 -	05/2014	0(O) -	0/0
664	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	154.50	08/2012 -	-	-	0/0
665	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	245.00	491.20	03/2008 01/2015	01/2015	82(O) 0(R)	0/0
666	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	254.30	06/2014 -	-	-	0/0
667	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	567.00	1,336.89	11/2013 -	-	-	0/0
668	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,TAMIL NADU	04/2011	571.00 -	571.00	-	10/2013 -	-	-	0/0
669	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	124.73	05/2013 -	-	-	0/0
670	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,KARNATAKA	11/2010	680.00 -	680.00	381.02	- -	-	-	2/2
671	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	993.84	03/2014 -	03/2014	0(O) -	0/0
672	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,JAMMU AND KASHMIR	12/2003	166.27 -	193.10	198.80	03/2008 -	-	-	0/0
673	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	193.45	58.35	11/2012 -	-	-	0/0
674	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	1,287.95	52.18	11/2015 -	11/2015	0(O) -	0/0
675	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	-	- -	-	-	0/0
	Total		96,437.15 -	98,553.21	80,641.13				12/27
	SHIPPING AND PORTS								
676	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY VESSELS - [N25000014]SHIPP.,MAHARASHTRA	10/2007	359.44 -	359.44	358.78	04/2011 11/2011	11/2011	-	0/0

Sector Wise Details

(March 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
677	ACQUISITION OF 4 NOS OF 82000 DWT KAMSAVMAX BULK CARRIERS FROM M/S JIANGSU EASTERN HEAVY INDUSTRIES - [N25000051]SHIPP.,MAHARASHTRA	08/2010	612.72 532.83	532.83	505.54	12/2012 11/2013	11/2013	-	0/0
678	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,MULTI STATE	07/2011	220.49 -	220.49	98.31	01/2013 06/2013	06/2013	-	0/0
679	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY - [N25000062]SHIPP.,MULTI STATE	01/2012	511.87 -	511.87	106.72	03/2014 08/2014	08/2014	5(O) 0(R)	0/0
680	ACQUISITION OF TWO NOS. OF 3060 DWT - [N25000043]SHIPP.,MAHARASHTRA	04/2009	277.03 280.00	277.03	294.87	12/2011 10/2012	10/2012	-	0/0
681	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053]SHIPP.,MAHARASHTRA	10/2010	966.46 -	994.82	427.54	02/2014 04/2014	04/2014	2(O) 0(R)	0/0
682	ACQUISITION OF THREE(3) NOS OF 6500TEU CELLULAR CONTAINER VESSELS FROM M/S STX SHIPBUILDING CO. LTD. - [N25000052]SHIPP.,MAHARASHTRA	10/2010	1,028.10 1,012.23	1,012.23	554.60	12/2013 11/2013	11/2013	-	0/0
683	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 1,460.00	2,158.16	1,004.31	12/2010 09/2012	10/2015	58(O) 37(R)	0/0
684	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,GUJARAT	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	-	0/0
685	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST - [N25000037]PORT TRUST,GUJARAT	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012	-	0/0
686	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL - [N25000003]PORT TRUST,MAHARASHTRA	10/2005	800.00 1,571.60	1,571.60	9.70	10/2008 -	-	-	0/0
687	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,ODISHA	12/2005	154.84 253.36	253.36	221.58	- 01/2009	12/2010	-	0/1
688	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 309.00	600.00	139.80	03/2006 06/2014	06/2014	99(O) 0(R)	0/0
689	MECHANIZATION OF COAL HANDLING FACILITIES TO 200000 DWT VESSELS ON DBFOT BASIS - [N25000049]PORT TRUST,ANDHRA PRADESH	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	-	0/0
690	MODIFICATION & STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST,GUJARAT	06/2010	277.00 -	277.00	0.21	03/2012 -	03/2012	-	0/0
691	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 298.17	373.22	371.18	04/2009 11/2009	02/2011	-	0/0
692	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	2,427.40	832.04	10/2008 11/2010	-	-	0/0
693	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN - [N25000048]PORT TRUST,KERALA	03/2009	3,500.00 4,150.00	4,150.00	3,661.95	01/2012 09/2012	08/2013	-	0/0
694	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST,GUJARAT	02/2011	830.00 -	621.53	-	05/2013 -	05/2013	-	0/0
	Total		15,617.12 -	18,600.58	8,807.06				0/1

Sector Wise Details

(March 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>TELECOMMUNICATIONS</u>								
695	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL,ASSAM	06/2007	336.81 -	336.81	183.16	01/2009 -	06/2014	65(O) -	0/0
696	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	384.00	29.45	10/2010 03/2012	03/2014	41(O) 24(R)	0/0
697	GSM EQUIPMENT OF 1625000LINES (2G) 325000 LINES 3(G) MP PHASE V.1 TELECOM CIRCLE - [N26000090]BSNL,MADHYA PRADESH	11/2009	916.70 -	930.60	828.80	11/2010 12/2012	09/2013	-	0/0
698	GSM EQUIPMENT OF 200000LINES (2G) UP(WEST)PHASE V.2 TELECOM CIRCLE - [N26000082]BSNL,UTTAR PRADESH	10/2008	336.84 -	336.84	-	10/2009 -	-	-	0/0
699	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTARANCHAL - [N26000058]BSNL,UTTARAKHAND	01/2009	149.15 -	158.72	84.68	06/2009 -	06/2014	60(O) -	0/0
700	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) PH-5.1 PUNJAB - [N26000041]BSNL,PUNJAB	02/2008	373.94 -	373.94	227.58	12/2008 -	12/2012	-	0/0
701	GSM EQUIPMENT OF 799000LINES (2G) 101000 LINES 3(G) JHARKHANDPHASE V.1 TELECOM CIRCLE - [N26000088]BSNL,JHARKHAND	03/2008	328.13 -	392.13	164.58	03/2009 -	01/2013	-	0/0
702	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK,PROCUREMENT OF GPON EQUIPMENT - [N26000073]BSNL,MULTI STATE	12/2007	152.65 -	152.65	-	03/2010 -	-	-	0/0
703	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK.PROCUREMENT OF GPON EQUIPMANT - [N26000072]BSNL,MULTI STATE	12/2007	952.88 -	952.88	-	03/2010 -	-	-	0/0
704	SUPPLY INSTALLATION TESTING AND COMMISSIONING OF RURAL WIMAX NETWORK PHASE-II - [N26000100]BSNL,MULTI STATE	07/2010	1,148.19 -	964.37	249.32	05/2011 -	05/2014	36(O) -	0/0
	Total		5,079.29 -	4,982.94	1,767.57				0/0
	<u>URBAN DEVELOPMENT</u>								
705	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA	05/2006	6,395.00 -	11,609.00	2,267.57	06/2011 -	03/2013	-	3/3
706	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA	02/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019	0(O) -	0/0
707	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI - [N28000048]CPWD,MAHARASHTRA	11/2006	114.18 173.08	173.08	-	04/2009 -	-	-	0/0
708	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	38,585.00	7,107.57	03/2016 -	03/2016	0(O) -	0/0
709	FARIDABAD EXTENSION - [N28000057]DMRC,DELHI	09/2011	2,494.00 -	2,494.00	551.23	09/2014 -	05/2015	8(O) -	0/0
	Total		73,993.32 -	79,266.22	9,926.37				3/3
	<u>WATER RESOURCES</u>								
710	PAGLADIYA DAM PROJECT - [300100001]MOWR,ASSAM	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012	-	0/0

Sector Wise Details									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	Total		542.90 -	1,187.00	35.49				0/0
	Grand Total		924,307.04	1,103,914.08	501,798.71				1095/3405

Sector wise current status of projects on the Flash Report

URBAN DEVELOPMENT


Current Status:

Number of Projects	5
Number of Projects On Schedule	2
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	2
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 5 projects, 2 projects are on schedule and 1 project are delayed .2 projects do not have fixed dates of commissioning.

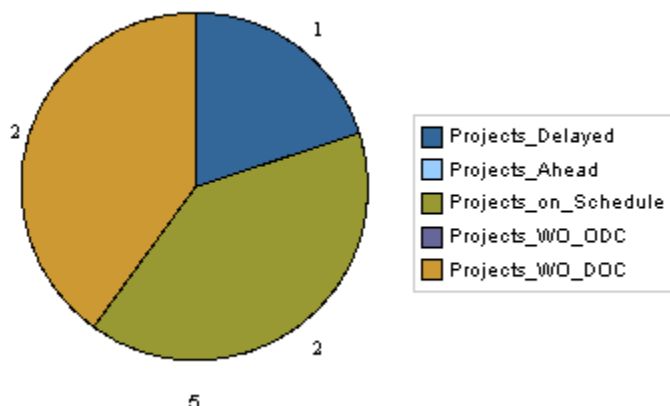

Investment Scenario

The Total Original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 73993.32 crore but this was subsequently revised to Rs. 79266.22 crore implying a cost overrun of 7.1%. The expenditure incurred on these projects till March, 2014 is Rs. 9926.37 crore, which is 12.5% of the revised cost of the projects.

Figures are in Rs. Crore

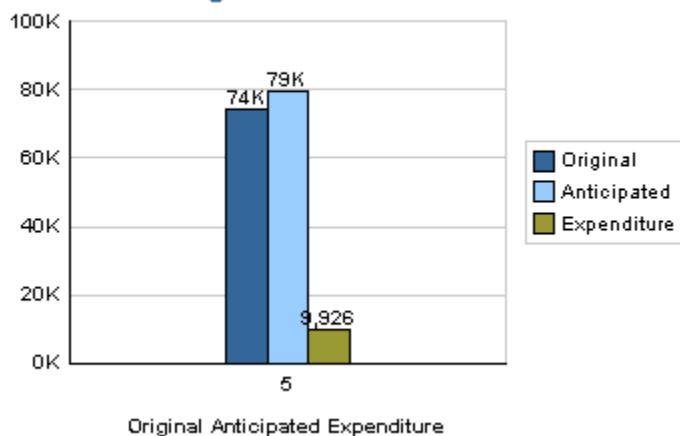

Sector wise current status of projects on the Flash Report


TELECOMMUNICATIONS

Current Status:

Number of Projects	10
Number of Projects Delayed	4
Number of Projects Without Date Of Commissioning	6


Brief Analysis

Project Status with respect to Original Schedule: Out of 10 projects, 4 projects are delayed .6 projects do not have fixed dates of commissioning.

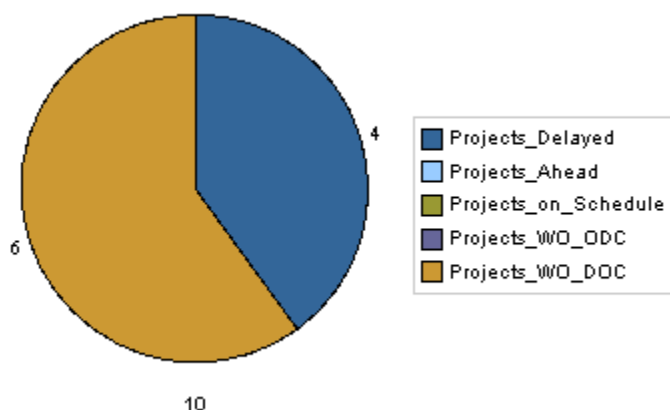

Investment Scenario

The Total Original cost of implementation of 10 projects when sanctioned, was of the order of Rs. 5079.29 crore but this was subsequently revised to Rs. 4982.94 crore implying a cost overrun of -1.9%. The expenditure incurred on these projects till March, 2014 is Rs. 1767.57 crore, which is 35.5% of the revised cost of the projects.

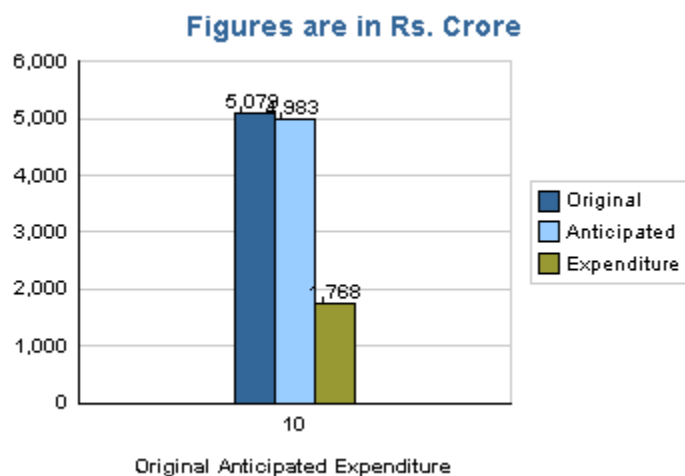

Sector wise current status of projects on the Flash Report

SHIPPING AND PORTS

Current Status:


Number of Projects **19**

Number of Projects Delayed **4**

Number of Projects Without Date Of Commissioning **15**

Brief Analysis


Project Status with respect to Original Schedule: Out of 19 projects, 4 projects are delayed .15 projects do not have fixed dates of commissioning.

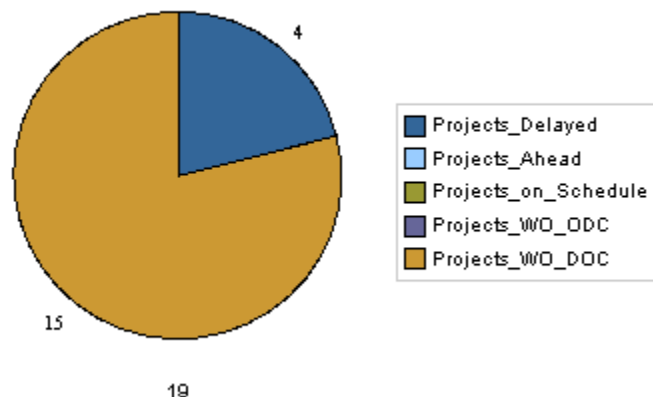

Investment Scenario

The Total Original cost of implementation of 19 projects when sanctioned, was of the order of Rs. 15617.12 crore but this was subsequently revised to Rs. 18600.58 crore implying a cost overrun of 19.1%. The expenditure incurred on these projects till March, 2014 is Rs. 8807.06 crore, which is 47.3% of the revised cost of the projects.

Figures are in Rs. Crore

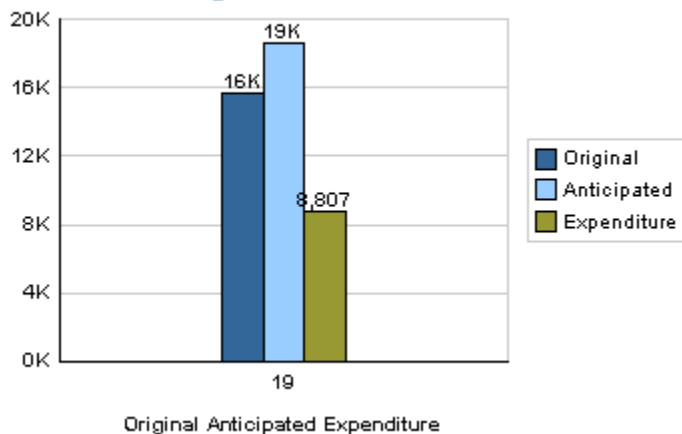

Sector wise current status of projects on the Flash Report

ROAD TRANSPORT AND HIGHW


Current Status:

Number of Projects	132
Number of Projects On Schedule	31
Number of Projects Delayed	19

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	81

Brief Analysis


Project Status with respect to Original Schedule: Out of 132 projects, 31 projects are on schedule and 19 projects are delayed .81 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

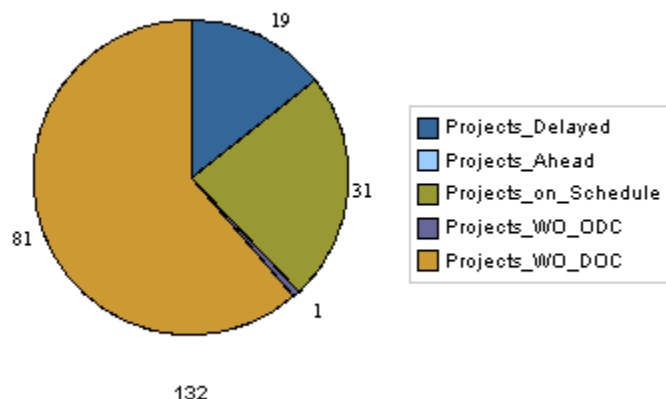

Investment Scenario

The Total Original cost of implementation of 132 projects when sanctioned, was of the order of Rs. 96437.15 crore but this was subsequently revised to Rs. 98553.21 crore implying a cost overrun of 2.2%. The expenditure incurred on these projects till March, 2014 is Rs. 80641.13 crore, which is 81.8% of the revised cost of the projects.

Figures are in Rs. Crore

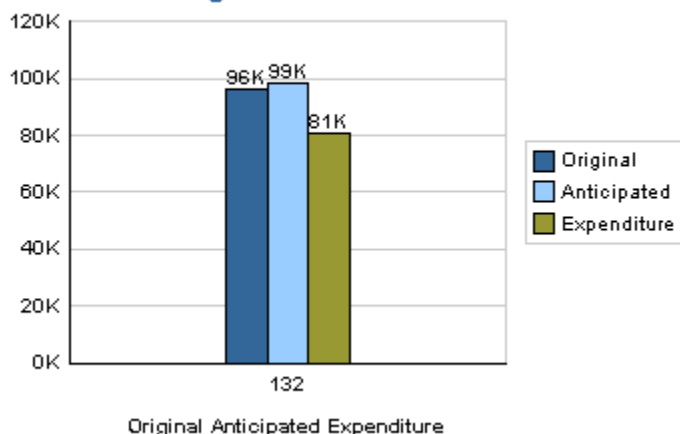

Sector wise current status of projects on the Flash Report

RAILWAYS


Current Status:

Number of Projects	282
Number of Projects On Schedule	15
Number of Projects Delayed	37

Number of Projects Without Original Date of Commissioning	21
Number of Projects Without Date Of Commissioning	209

Brief Analysis


Project Status with respect to Original Schedule: Out of 282 projects, 15 projects are on schedule and 37 projects are delayed .209 projects do not have fixed dates of commissioning.21 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

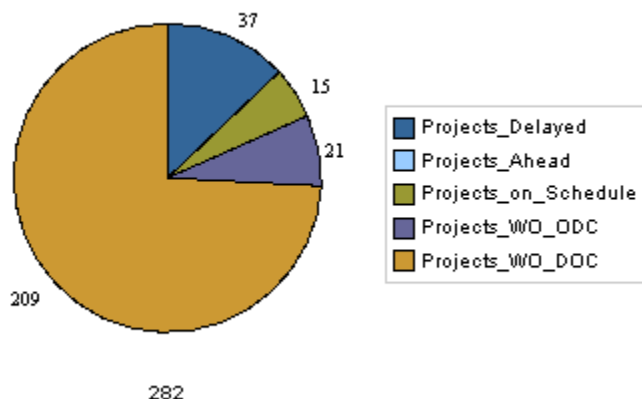

Investment Scenario

The Total Original cost of implementation of 282 projects when sanctioned, was of the order of Rs. 148551.55 crore but this was subsequently revised to Rs. 257231.72 crore implying a cost overrun of 73.2%. The expenditure incurred on these projects till March, 2014 is Rs. 77727.25 crore, which is 30.2% of the revised cost of the projects.

Figures are in Rs. Crore

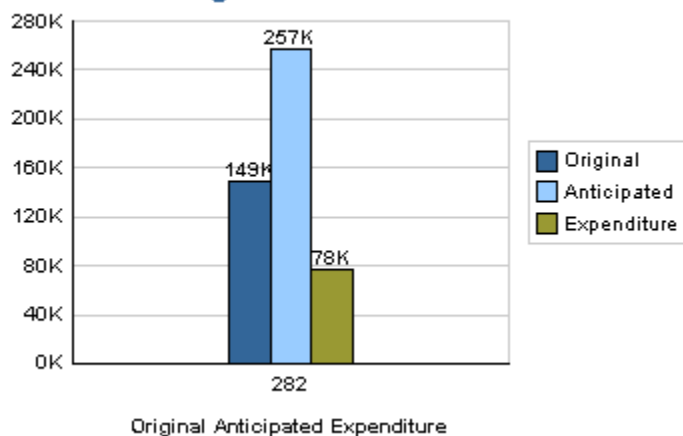

Sector wise current status of projects on the Flash Report

POWER


Current Status:

Number of Projects	96
Number of Projects On Schedule	36
Number of Projects Delayed	44
Number of Projects Ahead	2

Number of Projects Without Date Of Commissioning	14
--	----

Brief Analysis


Project Status with respect to Original Schedule: Out of 96 projects, 2 projects are ahead of schedule, 36 projects are on schedule and 44 projects are delayed .14 projects do not have fixed dates of commissioning.

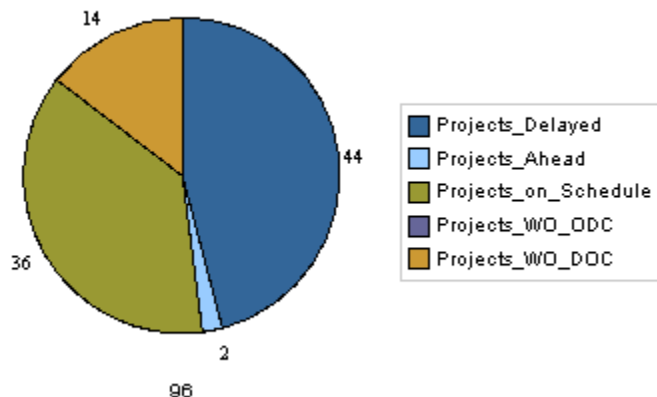

Investment Scenario

The Total Original cost of implementation of 96 projects when sanctioned, was of the order of Rs. 244469.88 crore but this was subsequently revised to Rs. 263493.12 crore implying a cost overrun of 7.8%. The expenditure incurred on these projects till March, 2014 is Rs. 114382.25 crore, which is 43.4% of the revised cost of the projects.

Figures are in Rs. Crore

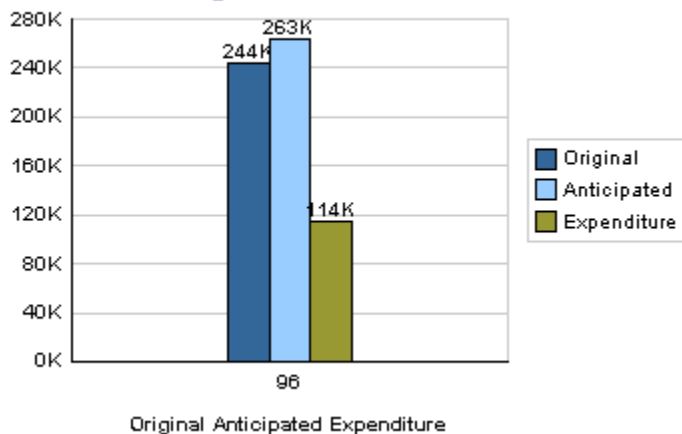

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	76
Number of Projects On Schedule	17
Number of Projects Delayed	50
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	7

Brief Analysis


Project Status with respect to Original Schedule: Out of 76 projects, 1 project are ahead of schedule, 17 projects are on schedule and 50 projects are delayed .7 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

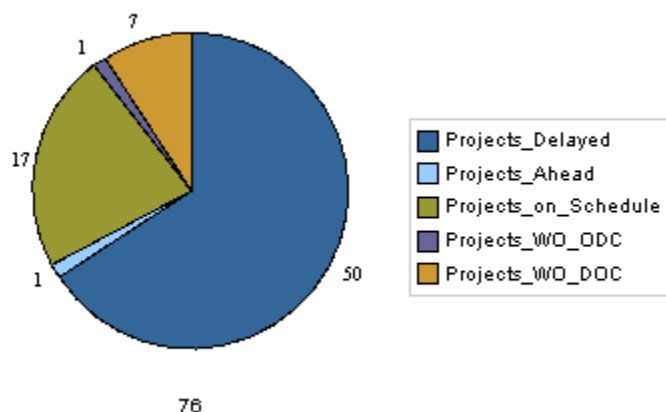

Investment Scenario

The Total Original cost of implementation of 76 projects when sanctioned, was of the order of Rs. 182981.12 crore but this was subsequently revised to Rs. 197259.22 crore implying a cost overrun of 7.8%. The expenditure incurred on these projects till March, 2014 is Rs. 100869.68 crore, which is 51.1% of the revised cost of the projects.

Figures are in Rs. Crore

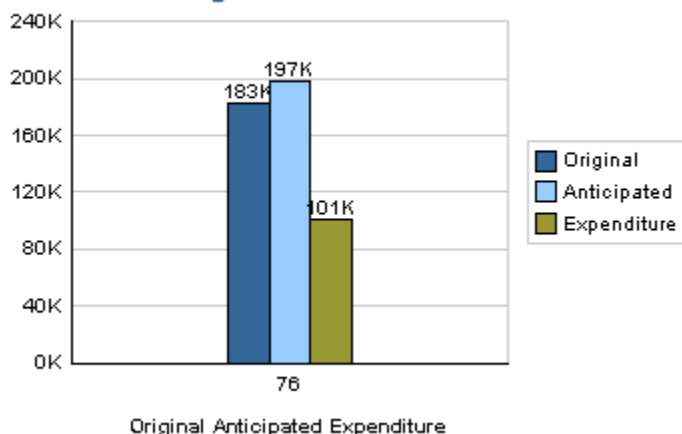

Sector wise current status of projects on the Flash Report

STEEL


Current Status:

Number of Projects	20
Number of Projects On Schedule	5
Number of Projects Delayed	13

Number of Projects Without Date Of Commissioning	2
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 20 projects, 5 projects are on schedule and 13 projects are delayed .2 projects do not have fixed dates of commissioning.

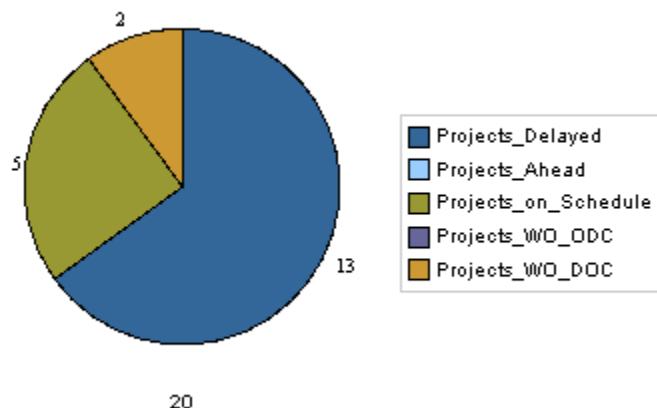

Investment Scenario

The Total Original cost of implementation of 20 projects when sanctioned, was of the order of Rs. 65959.26 crore but this was subsequently revised to Rs. 72188.55 crore implying a cost overrun of 9.4%. The expenditure incurred on these projects till March, 2014 is Rs. 59215.71 crore, which is 82% of the revised cost of the projects.

Figures are in Rs. Crore

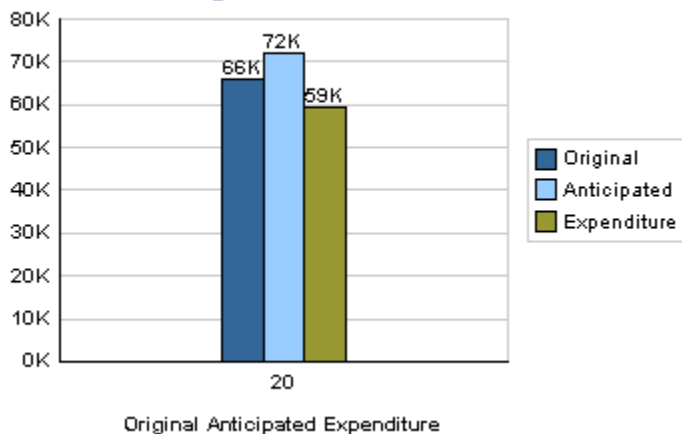

Sector wise current status of projects on the Flash Report

COAL


Current Status:

Number of Projects	56
Number of Projects On Schedule	24
Number of Projects Delayed	30

Number of Projects Without Date Of Commissioning 2

Brief Analysis


Project Status with respect to Original Schedule: Out of 56 projects, 24 projects are on schedule and 30 projects are delayed .2 projects do not have fixed dates of commissioning.

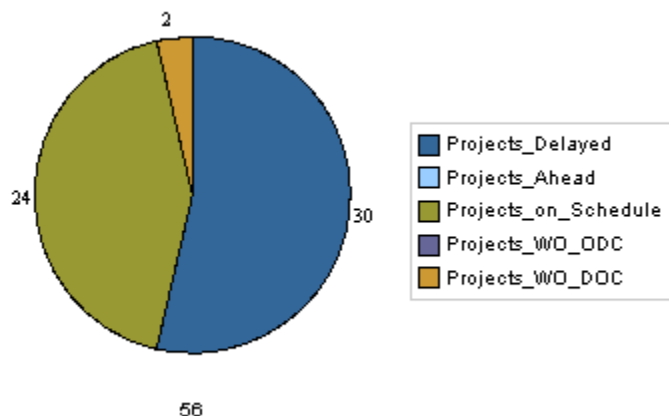

Investment Scenario

The Total Original cost of implementation of 56 projects when sanctioned, was of the order of Rs. 38737.38 crore but this was subsequently revised to Rs. 48559.52 crore implying a cost overrun of 25.4%. The expenditure incurred on these projects till March, 2014 is Rs. 17818.73 crore, which is 36.7% of the revised cost of the projects.

Figures are in Rs. Crore

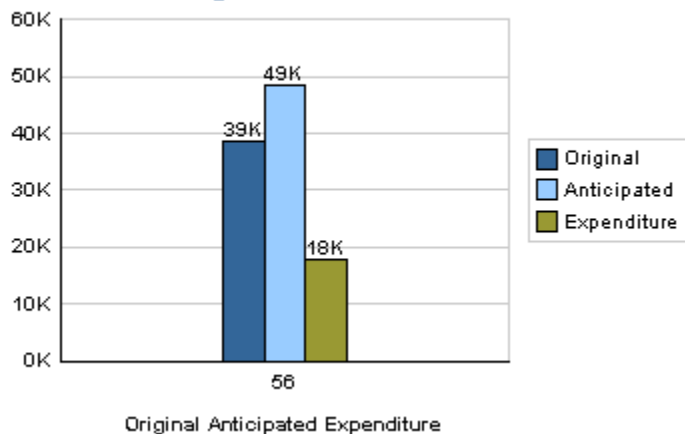

Sector wise current status of projects on the Flash Report

CIVIL AVIATION


Current Status:

Number of Projects	8
Number of Projects On Schedule	2
Number of Projects Delayed	3

Number of Projects Without Date Of Commissioning	3
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 8 projects, 2 projects are on schedule and 3 projects are delayed .3 projects do not have fixed dates of commissioning.

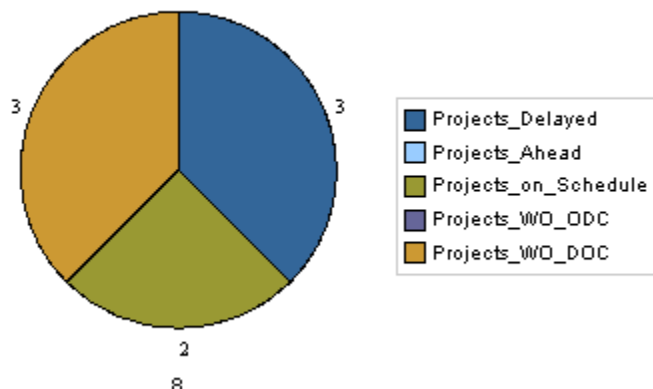

Investment Scenario

The Total Original cost of implementation of 8 projects when sanctioned, was of the order of Rs. 6035.46 crore but this was subsequently revised to Rs. 6946 crore implying a cost overrun of 15.1%. The expenditure incurred on these projects till March, 2014 is Rs. 5738.35 crore, which is 82.6% of the revised cost of the projects.

Figures are in Rs. Crore

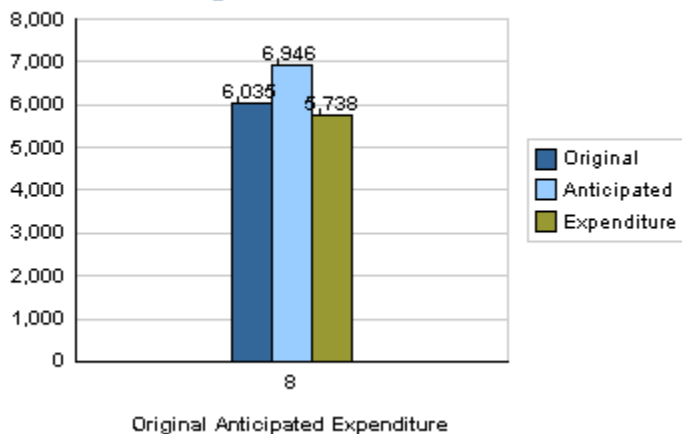

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	4

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed .

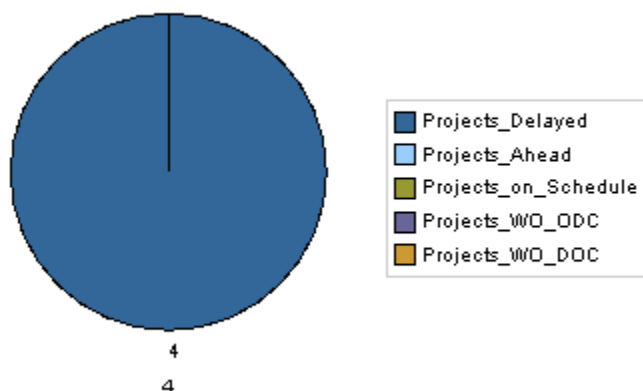

Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 40442 crore but this was subsequently revised to Rs. 46726 crore implying a cost overrun of 15.5%. The expenditure incurred on these projects till March, 2014 is Rs. 17198 crore, which is 36.8% of the revised cost of the projects.

Figures are in Rs. Crore

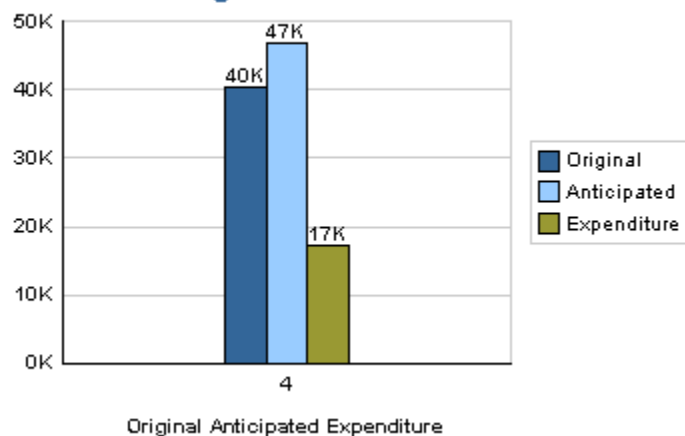

ANNEXURES

List of central sector projects

All Cost/Expenditure in Rs.crore

SN	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMMULATIVE EXPENDITURE
1	ANDHRA PRADESH	47	37177.32	45353.92	24676.72
2	ARUNACHAL PRADESH	4	9512.22	16855.73	10823.05
3	ASSAM	37	23180.22	34385.24	27259.24
4	BIHAR	45	32339.04	40462.85	29888.81
5	CHANDIGARH	1	452.00	452.00	230.42
6	CHHATISGARH	23	56979.13	64487.75	21168.60
7	DELHI	4	41533.88	41531.33	7713.12
8	GOA	1	335.61	388.53	278.32
9	GUJARAT	33	38022.74	39136.73	11917.39
10	HARYANA	8	4209.88	6407.61	7171.48
11	HIMACHAL PRADESH	5	13845.21	20316.02	12451.10
12	JAMMU AND KASHMIR	7	11965.40	30895.56	15012.63
13	JHARKHAND	27	16118.82	20383.55	11294.60
14	KARNATAKA	34	79459.69	91331.44	27987.39
15	KERALA	12	22610.65	25135.43	8815.02
16	MADHYA PRADESH	19	30777.43	32003.81	10087.48
17	MAHARASHTRA	51	93259.91	108834.44	51630.32
18	MANIPUR	1	727.56	4478.17	2023.83
19	MEGHALAYA	3	4845.02	4845.02	910.37
20	MIZORAM	2	1532.97	3307.11	744.71
21	MULTI STATE	171	182037.73	204897.80	73492.03
22	NAGALAND	2	5124.00	5124.00	9.24
23	ODISHA	28	55789.04	62373.13	40040.67
24	PUNJAB	4	1680.20	1680.20	2500.49
25	RAJASTHAN	25	25380.48	25805.94	9690.45
26	SIKKIM	2	1648.94	3690.04	352.48
27	TAMIL NADU	38	51742.73	67974.43	40727.02
28	TRIPURA	6	2966.26	3987.74	2631.13
29	UTTAR PRADESH	28	21357.79	25954.00	14369.71
30	UTTARAKHAND	6	7844.04	10085.07	2956.93
31	WEST BENGAL	36	49851.13	61349.49	32943.96
Total		710	924307.04	1103914.08	501798.71

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
1	KUDANKULAM APP (NPCIL)	ATOMIC ENERGY	12/2001	13,171	-	17,198
2	PARBATI HEP (NHPC) II	POWER	09/2002	3,919.59	-	4,373.85
3	SUBANSIRI LOWER H.E.P (NHPC)	POWER	09/2003	6,285.33	-	6,788.54
4	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	POWER	12/2004	2,496.9	-	2,816.4
5	BARH STPP(3X660MW) NTPC	POWER	12/2003	8,692.97	-	9,238
6	TEESTA LOW DAM HEP, STAGE-IV (NHPC)	POWER	09/2005	1,061.38	-	1,482.62
7	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL)	POWER	03/2005	596.45	-	929.66
8	PARBATI H.E.P. STAGE -III (NHPC)	POWER	10/2005	2,304.56	-	2,349.46
9	VIRAMGAM-BHILDI(WR), GC	RAILWAYS	04/1990	155.66	-	200.15
10	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	RAILWAYS	12/1994	124.43	495.68	663.66
11	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	RAILWAYS	03/1995	2,500	2500	8,822.5
12	CALICUT-MANGALORE (DL) (SR)	RAILWAYS	02/1996	240	-	599.4
13	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR	RAILWAYS	02/1997	295	412.91	872.87
14	KARUR-SALEM(NL), SR	RAILWAYS	02/1997	155.55	155	773.42

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
15	NANDYAL-YERRAGUNTLA(NL), SCR	RAILWAYS	03/1996	155.74	429.49	679.45
16	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES, NEFR	RAILWAYS	09/1997	1,000	1500	3,092.23
17	RANCHI-LOHARDAGA(GC), SER	RAILWAYS	04/1997	194.07	194.07	371.5
18	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	RAILWAYS	04/1997	233	501.69	732.63
19	GULBARGA-BIDAR, SCR(NL)	RAILWAYS	02/1998	242.42	369.7	402.47
20	JALANDHAR-PATHANKOT- JAMMU-TAWI (LD), NR	RAILWAYS	03/2002	409	625.3	837.7
21	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	RAILWAYS	09/1995	100	100	566.35
22	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	RAILWAYS	03/1998	280	-	834.61
23	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	RAILWAYS	04/2000	733	733	1,552.32
24	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	RAILWAYS	03/2000	907.69	3156.32	3,485.95
25	GADWAL - RAICHUR (NL), SCR	RAILWAYS	04/1998	92.63	-	293.11
26	JIND-SONEPAT (NL), NR	RAILWAYS	01/2004	190.81	238.56	544.86
27	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	RAILWAYS	04/2003	727.56	727.53	2,023.83
28	DANIAWAN-BIHARSARIF (NL), ECR	RAILWAYS	04/2001	104.79	-	145.42

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
29	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	RAILWAYS	01/2004	915.7	915.7	2,664.89
30	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	ROAD TRANSPORT AND HIGHWAYS	12/2003	157.47	157.47	260.3
31	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31C	ROAD TRANSPORT AND HIGHWAYS	12/2003	230	-	240.09
32	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80	ROAD TRANSPORT AND HIGHWAYS	12/2003	166.27	-	198.8
33	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	195	-	262.98
34	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	237.8	-	292.51
35	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	332.94	-	511.54
36	KOTA BYPASS,RJ-4, NH-76 (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	275	-	283.31
37	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	251.03	-	351.82
38	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT	CIVIL AVIATION	08/2008	1,942.51	2325	2,537.92
39	EXPANSION OF IISCO STEEL PLANT	STEEL	06/2008	14,443	-	15,787.87
40	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I	PETROLEUM	07/2009	238.68	-	293.12
41	ASSAM GAS CRACKER PROJECT	PETROCHEMICALS	04/2006	5,460.61	-	7,671.12
42	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT	PETROLEUM	08/2009	246.81	-	258.57

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
43	PARE HYDRO ELECTRIC PROJECT	POWER	12/2008	573.99	-	811.78
44	TRIPURA GAS BASED POWER PROJECT	POWER	07/2009	421.01	623.44	745.55
45	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT	PETROLEUM	08/2008	144.02	-	154.08
46	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	RAILWAYS	04/1996	114.01	332.92	451.33
47	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	RAILWAYS	09/2006	343.17	343.17	744.56
48	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	RAILWAYS	12/2006	170	170	417.49
49	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR	RAILWAYS	09/1996	156	156	406.33
50	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	RAILWAYS	04/2007	482	482.7	560.17
51	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	RAILWAYS	04/1996	1,676.31	1676.31	4,020.98
52	RAJKOT-VERAVAL, WANSJALIA TO JATASAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	RAILWAYS	04/1994	320.66	-	461.85
53	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR	RAILWAYS	04/2013	456	-	558
54	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	RAILWAYS	04/2010	739.65	-	787.83
55	SAKRI-HASANPUR ROAD (NL)	RAILWAYS	04/1999	175.69	-	240.38
56	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	RAILWAYS	04/1999	198.68	-	266.66

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
57	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	RAILWAYS	04/1999	271.24	-	461.3
58	NEW BG LINE FROM DUDHNOI-MENDIPATAR	RAILWAYS	04/1999	175.43	-	220.68
59	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	RAILWAYS	04/1999	895	-	955.94
60	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	RAILWAYS	04/2007	247	-	540.5
61	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI	RAILWAYS	04/1999	523.17	-	947.86
62	PANVEL PEN DOUBLING	RAILWAYS	04/2006	191	-	217.77
63	MUNIRABAD (GINGERA) -RAICHUR NL	RAILWAYS	04/2007	179.65	-	256.61
64	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI	RAILWAYS	04/1999	460.94	-	800.9
65	NALBARI TO BIJNI (AS-8)	ROAD TRANSPORT AND HIGHWAYS	12/2003	200	-	308.16
66	GUWHATI TO NALBARI (AS-4)	ROAD TRANSPORT AND HIGHWAYS	12/2003	175.96	-	249.37
67	NAGAON TO DHARAMTUL (AS-2)	ROAD TRANSPORT AND HIGHWAYS	12/2003	264.72	-	303.05
68	SONAPUR TO GUWAHTI (AS-3)	ROAD TRANSPORT AND HIGHWAYS	12/2003	245	-	491.2
69	GUWAHATI TO NALBARI (AS-5)	ROAD TRANSPORT AND HIGHWAYS	12/2003	198.16	-	306.31
70	NALBARI TO BIJNI (AS-6)	ROAD TRANSPORT AND HIGHWAYS	12/2003	225	-	269.79

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
71	NALBARI T BIJNI (AS-7)	ROAD TRANSPORT AND HIGHWAYS	12/2003	208	230	313.93
72	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	ROAD TRANSPORT AND HIGHWAYS	12/2003	160	-	209.92
73	DHARAMTUL TO SONAPUR (AS-19)	ROAD TRANSPORT AND HIGHWAYS	12/2003	200	-	257.33
74	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	ROAD TRANSPORT AND HIGHWAYS	03/2005	557	-	1,129.29
75	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	ROAD TRANSPORT AND HIGHWAYS	12/2003	232.45	-	308.97
76	DELHI/ HARYANA BORDER TO ROHTAK	ROAD TRANSPORT AND HIGHWAYS	04/2007	486	-	661.58
77	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	ROAD TRANSPORT AND HIGHWAYS	03/2005	940	-	1,339.69
78	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	ROAD TRANSPORT AND HIGHWAYS	03/2010	1,509.1	-	2,021.74
79	PUNE-SHOLAPUR, PKG1	ROAD TRANSPORT AND HIGHWAYS	11/2009	1,110	-	1,825.57
80	KISHANGARH-AJMER-BEAWER	ROAD TRANSPORT AND HIGHWAYS	11/2009	795	-	1,128.18
81	CHENNAI-TADA(SIX LANE)	ROAD TRANSPORT AND HIGHWAYS	04/2009	353.37	-	446.24
82	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15)	ROAD TRANSPORT AND HIGHWAYS	05/2009	572.3	-	886.91
83	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	ROAD TRANSPORT AND HIGHWAYS	05/2009	1,108	-	3,466
84	JAIPUR-TONK-DEOLI	ROAD TRANSPORT AND HIGHWAYS	06/2010	792.06	-	1,980.9

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
85	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	ROAD TRANSPORT AND HIGHWAYS	09/2010	946	-	1,077.27
86	TALEGAON-AMRAVATI	ROAD TRANSPORT AND HIGHWAYS	11/2009	567	-	1,336.89
87	HAZARIBAGH-RANCHI	ROAD TRANSPORT AND HIGHWAYS	08/2010	625.07	-	995.85
88	ARMUR TO KADLOOR YELLAREDDY	ROAD TRANSPORT AND HIGHWAYS	02/2010	390.56	-	772.4
89	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	ROAD TRANSPORT AND HIGHWAYS	09/2010	852	-	864.53
90	KUNDUPUR-SURATHKAL & MANGLORE	ROAD TRANSPORT AND HIGHWAYS	09/2010	671	-	938.4
91	AMRITSAR-PATHANKOT	ROAD TRANSPORT AND HIGHWAYS	05/2010	705	-	2,182.6
92	DEOLI-KOTA	ROAD TRANSPORT AND HIGHWAYS	01/2011	593	-	685.53
93	PANIPAT-ROHTAK	ROAD TRANSPORT AND HIGHWAYS	04/2011	807	-	1,325.75
94	DEVIHALLI-HASSAN	ROAD TRANSPORT AND HIGHWAYS	12/2010	453	-	761.25
95	MURADABAD-BAREILY	ROAD TRANSPORT AND HIGHWAYS	04/2010	1,267	-	2,122.23
96	BELGAUM-DHARWAD(NH-4)	ROAD TRANSPORT AND HIGHWAYS	12/2010	480	-	649.04
97	INDORE-DEWAS(NH-3)	ROAD TRANSPORT AND HIGHWAYS	11/2010	325	-	574.8
98	2 LANNING OF MOKAMA-MUNGER	ROAD TRANSPORT AND HIGHWAYS	05/2011	351.54	-	394.67

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
99	4 LANNING OF AHMEDABAD TO GODHARA	ROAD TRANSPORT AND HIGHWAYS	12/2010	1,008.5	-	1,356.04
100	4 LANNING OF GODHARA TO GUJARAT/MP BORDER	ROAD TRANSPORT AND HIGHWAYS	03/2011	785.5	-	848.81
101	ROHTAK-BAWAL	ROAD TRANSPORT AND HIGHWAYS	05/2011	650	-	1,160.37
102	GHAZIABAD-ALIGARH NH-91	ROAD TRANSPORT AND HIGHWAYS	02/2011	1,141	1141	1,319.54
103	JORBAT - BARAPANI	ROAD TRANSPORT AND HIGHWAYS	01/2011	536	-	574.5
104	2-LANNING OF SHILONG BYPASS	ROAD TRANSPORT AND HIGHWAYS	02/2011	226	-	332.5
105	2-LANNING WITH PS KHAGARIA-PURNEA	ROAD TRANSPORT AND HIGHWAYS	05/2011	664	-	688.13
106	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	ROAD TRANSPORT AND HIGHWAYS	09/2011	574	-	794.16
107	4-LANNING OF CHAPRA-HAJIPUR	ROAD TRANSPORT AND HIGHWAYS	01/2011	575	-	819.07
108	2 LANNING OF MUZAFFARPUR - SONBARSA	ROAD TRANSPORT AND HIGHWAYS	05/2011	511.54	-	687.49
109	4-LANING OF BARHI-HAZARIBAGH	ROAD TRANSPORT AND HIGHWAYS	02/2012	398	-	457.03
110	BHUBANESWAR TO PURI	ROAD TRANSPORT AND HIGHWAYS	03/2011	500.29	-	579.27
111	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER	ROAD TRANSPORT AND HIGHWAYS	11/2011	909	-	959.15
112	JAIPUR-REENGUS	ROAD TRANSPORT AND HIGHWAYS	08/2010	267.81	-	685.86

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
113	4-LANING OF FARAKA-RAIGANJ	ROAD TRANSPORT AND HIGHWAYS	02/2011	1,078.84	-	1,469.16
114	4-LANING OF BRAHAMPORE-FARAKA	ROAD TRANSPORT AND HIGHWAYS	02/2011	998.79	-	1,486.08
115	2 LANING WITH PS AGRA ALIGARH	ROAD TRANSPORT AND HIGHWAYS	10/2012	250.5	-	328.56
116	ACQUISITION OF TWO NOS. OF 3060 DWT	SHIPPING AND PORTS	04/2009	277.03	280	294.87
117	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	SHIPPING AND PORTS	03/2007	245.67	298.17	371.18

List of Projects Ahead of Schedule w.r.t. Original Schedule

							(March 2014)
						Date of Commissioning	
S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>POWER</u>						
1	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144	9/2012	1,508.74	1,508.74	247.12	06/2016	12/2015
	Total		1,508.74	1,508.74	247.12		
	<u>PETROLEUM</u>						
2	LPG TERMINAL AT KOCHI - [N16000171	12/2012	607.06	607.06	20.38	01/2016	12/2015
	Total		607.06	607.06	20.38		
	<u>POWER</u>						
3	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137	9/2012	1,935.35	1,935.35	605.31	12/2014	11/2014
	Total		1,935.35	1,935.35	605.31		
	Grand Total		4,051.15	4,051.15	872.81		

List of Projects Without Original Date of Commissioning

(March 2014)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>PETROLEUM</u>								
1	SURAT PARADIP PIPELINE PROJECT - [N16000163]GAIL,MULTI STATE	10/2012	10,281.00 -	10,281.00	1.36	- -	04/2015	-	0/0
	Total		10,281.00 -	10,281.00	1.36				0/0
	<u>RAILWAYS</u>								
2	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	151.84 410.08	410.08	242.95	- -	03/2014	-	0/0
3	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 377.32	645.00	225.04	- -	03/2014	-	0/0
4	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	323.40 744.71	744.71	521.04	- -	03/2014	-	0/1
5	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 230.03	230.03	151.26	- -	03/2014	-	0/0
6	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR - [N22000083]NEFR,ARUNACHAL PRADESH	09/1996	156.00 156.00	406.40	406.33	- -	03/2014	-	0/0
7	NEW BG LINE FROM DUDHNOI-MENDIPATAR - [N22000192]NEFR,MULTI STATE	04/1999	175.43 -	175.43	220.68	- -	03/2014	-	0/0
8	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	203.00 -	203.00	177.40	- -	03/2014	-	0/0
9	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	279.40	188.74	- -	04/2014	-	0/0
10	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	191.00 -	260.16	217.77	- -	05/2014	-	0/0
11	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	355.38 470.21	1,995.25	295.81	- -	12/2014	-	0/0
12	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00 -	951.24	540.50	- -	12/2014	-	0/0
13	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NEFR,WEST BENGAL	04/1983	36.80 274.41	703.17	252.52	- -	03/2015	-	0/0
14	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]NEFR,MULTI STATE	01/2004	915.70 915.70	2,232.50	2,664.89	- -	03/2015	-	0/0
15	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,BIHAR	04/2008	282.92 282.92	359.86	2.22	- -	03/2015	-	0/0
16	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 -	258.20	1.18	- -	03/2016	-	0/0
17	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NEFR,MULTI STATE	04/2010	241.52 -	241.52	148.33	- -	03/2016	-	0/0

(March 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
18	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NEFR,ASSAM	04/2011	312.12 -	312.12	76.43	- -	03/2016	-	0/0
19	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NEFR, WEST BENGAL	04/2011	209.77 -	209.77	34.24	- -	03/2017	-	0/0
20	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NEFR, WEST BENGAL	04/2012	283.55 -	283.55	1.14	- -	03/2017	-	0/0
21	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	714.10	18.16	- 12/2017	12/2017	0(R3)	0/0
22	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NEFR, ASSAM	09/2006	200.00 200.00	385.20	181.12	- -	03/2018	-	0/0
	Total		5,985.40 -	12,000.69	6,567.75				0/1
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
23	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI, KARNATAKA	09/2010	671.00 -	671.00	938.40	- -	06/2014	-	2/3
	Total		671.00 -	671.00	938.40				2/3
	Grand Total		16,937.40	22,952.69	7,507.51				2/4

List of Projects Without Date of Commissioning

					Date of Commissioning
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>CIVIL AVIATION</u>				
1	D/O KAMARAJ DOMESTIC TER-PH-II AND EXP. ANNA INT. TER BLDG(K1) - [N04000038]AAI,TAMIL NADU	08/2008	1,808.00 2,015.00	01/2011 02/2012	02/2012
2	C/O INTEGRATED PASSENGER TER. BULD. NSCB AIRPORT - [N04000037]AAI, WEST BENGAL	08/2008	1,942.51 2,325.00	05/2011 -	03/2013
3	GAGAN PROJECT - [N04000065]AAI,MULTI STATE	09/2008	626.00 -	06/2013 -	06/2013
	Total		4,376.51 -		
	<u>COAL</u>				
4	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,ANDHRA PRADESH	10/2006	249.03 -	03/2012 -	-
5	JALLARAM SHAFT PROJECT - [N06000025]SCCL,ANDHRA PRADESH	09/2007	467.78 -	03/2013 -	-
	Total		716.81 -		
	<u>STEEL</u>				
6	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,ANDHRA PRADESH	08/2006	260.00 349.64	12/2009 08/2010	06/2013
7	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT EXP. UNIT - [N12000068]RINL,ANDHRA PRADESH	07/2007	202.00 343.58	01/2010 02/2011	11/2013
	Total		462.00 -		
	<u>PETROCHEMICALS</u>				
8	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,ASSAM	04/2006	5,460.61 -	04/2012 -	-
	Total		5,460.61 -		
	<u>PETROLEUM</u>				
9	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I - [N16000070]GAIL,MULTI STATE	07/2009	238.68 -	01/2012 -	07/2013
10	DABHOL BANGALORE PIPELINE PROJECT PHASE-II - [N16000147]GAIL,MULTI STATE	06/2009	486.00 -	09/2013 -	09/2013
11	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]MANGALORE REFIN,KARNATAKA	07/2010	1,043.57 -	04/2012 -	12/2013
12	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA	12/2009	1,584.00 -	- -	-
13	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,MULTI STATE	12/2009	540.92 -	07/2012 07/2012	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
14	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00 -	12/2012 -	-
15	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	- -	-
	Total		7,519.17 -		
	<u>POWER</u>				
16	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	09/2008 -	03/2013
17	MOUDA STPP - [N18000048]NTPC,MAHARASHTRA	11/2008	5,459.28 -	08/2012 -	03/2013
18	VINDHYACHAL STTP STAGE-IV - [N18000072]NTPC,MADHYA PRADESH	01/2009	5,915.00 -	10/2012 -	03/2013
19	RIHAND STTP STAGE-III (2X500MW) - [N18000073]NTPC,UTTAR PRADESH	01/2009	6,230.81 -	10/2012 -	10/2013
20	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	02/2012 -	12/2013
21	RAMPUR HEP(412 MW) - [N18000024]SJVN, HIMACHAL PRADESH	01/2007	2,047.03 -	01/2012 -	-
22	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	11/2011 -	-
23	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,MULTI STATE	02/2009	184.19 -	11/2011 -	-
24	SYSTEM STRENGTHENING -XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	06/2012 -	-
25	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,MADHYA PRADESH	08/2011	425.51 -	10/2013 -	-
26	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000107]PGCIL,CHHATISGARH	08/2011	1,391.97 -	12/2013 -	-
27	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118]PGCIL,GUJARAT	01/2012	259.28 -	01/2014 -	-
28	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]NEEPCO,TRIPURA	07/2012	296.87 -	- -	-
29	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,KARNATAKA	03/2005	596.45 -	12/2007 12/2009	-
	Total		25,737.97 -		
	<u>RAILWAYS</u>				
30	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	409.00 625.30	06/2007 -	06/2007
31	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,ANDHRA PRADESH	07/1998	125.00 -	07/2008 -	07/2008
32	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	- 05/2009	05/2009
33	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	371.36 768.87	- 03/2010	03/2010

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
34	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT (MTP) - [220100268]MRTP, WEST BENGAL	03/2000	907.69 3,156.32	12/2006 08/2010	08/2010
35	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	225.68 293.74	12/2010 12/2010	12/2010
36	AMRAVATI-NARKHER NL(CR) - [220100118]CR, MAHARASHTRA	06/1994	120.90 663.01	06/1999 03/2011	03/2011
37	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR, MULTI STATE	12/2006	170.00 170.00	03/2011 03/2011	03/2011
38	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011
39	CALICUT-MANGALORE (DL) (SR) - [220100151]SR, MULTI STATE	02/1996	240.00 -	- -	02/2012
40	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	157.96 1,188.91	- 12/2009	02/2012
41	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	259.51 533.38	12/2011 02/2012	02/2012
42	NANDYAL-YERRAGUNTLA(NL), SCR - [220100192]SCR, ANDHRA PRADESH	03/1996	155.74 429.49	02/2009 -	03/2012
43	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER, UTTAR PRADESH	03/2002	381.17 863.23	- -	03/2012
44	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N22000052]WS&PU, BIHAR	04/2003	98.74 224.51	- -	03/2012
45	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU, BIHAR	03/2005	470.09 1,417.97	- -	03/2012
46	KARUR-SALEM(NL), SR - [220100191]SR, TAMIL NADU	02/1997	155.55 155.00	- -	10/2012
47	JIND-SONEPAT (NL), NR - [220100280]NR, HARYANA	01/2004	190.81 238.56	03/2012 03/2012	12/2012
48	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR, TAMIL NADU	09/2006	343.17 343.17	- -	12/2012
49	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR - [220100183]SWR, KARNATAKA	02/1997	295.00 412.91	- -	01/2013
50	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER, MULTI STATE	04/2000	138.00 607.09	12/2012 12/2012	02/2013
51	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER, BIHAR	04/2003	218.19 218.19	- -	02/2013
52	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER, JHARKHAND	04/2008	167.73 -	03/2012 -	02/2013
53	MANDARHILL-DUMKA-RAMPURHAT (NL), ER - [220100168]ER, JHARKHAND	04/1995	184.00 900.05	12/2011 12/2011	03/2013
54	KANPUR-KASGANJ-MATHURA(GC), NER - [220100197]NER, UTTAR PRADESH	03/1997	395.00 1,577.45	- -	03/2013
55	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR, MULTI STATE	03/1998	280.00 -	- -	03/2013
56	GADWAL - RAICHUR (NL), SCR - [220100270]SCR, MULTI STATE	04/1998	92.63 -	02/2011 02/2011	03/2013
57	KOSI BRIDGE (NL), ECR - [220100304]ECR, BIHAR	04/2002	323.41 322.95	03/2012 03/2013	03/2013
58	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR, BIHAR	04/1996	114.01 332.92	03/2012 03/2013	03/2013

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
59	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	03/2013 -	03/2013
60	GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL	04/2009	189.97 -	12/2011 11/2013	11/2013
61	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- -	12/2013
62	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	03/1994 -	01/2014
63	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,ANDHRA PRADESH	12/1994	124.43 495.68	- -	02/2014
64	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-
65	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,038.00	03/1998 -	-
66	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	- -	-
67	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	- 09/2009	-
68	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 418.17	- -	-
69	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-
70	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-
71	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	03/2010 -	-
72	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
73	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	-
74	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	-
75	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	160.89 199.75	- -	-
76	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 295.00	- -	-
77	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
78	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	- -	-
79	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-
80	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	- -	-
81	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	- -	-
82	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	- -	-
83	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
84	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR, GUJARAT	04/1994	320.66 -	- -	-
85	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR, GUJARAT	04/2013	1,266.89 -	- -	-
86	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR, GUJARAT	04/2011	446.00 -	- -	-
87	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR, MULTI STATE	04/2012	2,082.75 -	- -	-
88	THIYAT HAMIRA-SANU - [N22000149]NWR, RAJASTHAN	04/2013	236.93 -	- -	-
89	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR, RAJASTHAN	04/2013	822.00 -	- -	-
90	PUSHKAR-MERTA - [N22000151]NWR, RAJASTHAN	04/2013	323.00 -	- -	-
91	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR, RAJASTHAN	04/2013	456.00 -	- -	-
92	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR, RAJASTHAN	04/2010	739.65 -	- -	-
93	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR, RAJASTHAN	04/2011	239.73 -	- -	-
94	AJMER-BANGURGRAM - [N22000155]NWR, RAJASTHAN	04/2011	213.39 -	- -	-
95	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR, RAJASTHAN	04/2012	288.97 -	- -	-
96	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR, RAJASTHAN	04/2013	242.09 -	- -	-
97	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	- -	-
98	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SWR, MULTI STATE	04/2010	553.63 -	- -	-
99	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL	04/2011	289.64 -	- -	-
100	ARA-BHABHUA ROAD (NL) - [N22000166]SER, BIHAR	04/2008	490.80 -	- -	-
101	NAWADA-LAXMIPUR (NL) - [N22000167]SER, BIHAR	04/2008	620.57 -	- -	-
102	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR, BIHAR	04/2008	445.25 -	- -	-
103	GAYA-CHATRA (NL) - [N22000169]ECOR, MULTI STATE	04/2008	415.67 -	- -	-
104	BIHTA-AURANGABAD (NL) - [N22000170]ECOR, BIHAR	04/2008	326.20 -	- -	-
105	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR, BIHAR	04/1999	175.69 -	- -	-
106	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR, BIHAR	04/2006	285.07 -	- -	-
107	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR, BIHAR	04/2005	366.73 -	- -	-
108	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR, BIHAR	04/2006	211.00 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
109	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-
110	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-
111	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-
112	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-
113	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
114	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-
115	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-
116	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-
117	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NEFR,MULTI STATE	04/2013	1,798.00 -	- -	-
118	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	- -	-
119	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-
120	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
121	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-
122	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1999	271.24 -	- -	-
123	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	- -	-
124	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-
125	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
126	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NEFR,WEST BENGAL	04/2010	221.42 -	- -	-
127	AGARTALA-AKHAURA NL - [N22000195]NEFR,TRIPURA	04/2012	252.00 -	- -	-
128	DIMAPUR-TIZIT NL - [N22000196]NEFR,NAGALAND	04/2013	4,274.00 -	- -	-
129	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
130	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-
131	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-
132	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-
133	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NEFR,MEGHALAYA	04/2010	4,083.02 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
134	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NEFR,MULTI STATE	04/2010	242.22 -	- -	-
135	MURKONGSELEK-PASIGHAT NL - [N22000208]NEFR,MULTI STATE	04/2011	165.82 -	- -	-
136	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NEFR,MULTI STATE	04/1999	523.17 -	- -	-
137	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NEFR,ASSAM	04/2012	246.07 -	- -	-
138	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSHUPUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-
139	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-
140	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1999	406.99 -	- -	-
141	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-
142	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-
143	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-
144	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-
145	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-
146	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-
147	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-
148	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-
149	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-
150	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-
151	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-
152	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-
153	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	697.00 -	- -	-
154	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-
155	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-
156	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
157	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-
158	SAINTIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-
159	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-
160	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-
161	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-
162	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-
163	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-
164	NABADWIPDHAM-PATULI DOUBLING - [N22000246]ER,MULTI STATE	04/2010	169.82 -	- -	-
165	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	182.06 -	- -	-
166	SANTOSHPUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-
167	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-
168	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-
169	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-
170	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-
171	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	- -	-
172	MANUGURU-RAMAGUNDAM - [N22000259](SCR),ANDHRA PRADESH	04/2013	1,112.00 -	- -	-
173	KONDAPALLI-PENUBALLI - [N22000260](SCR),ANDHRA PRADESH	04/2013	723.00 -	- -	-
174	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261](SCR),MULTI STATE	04/2012	1,054.35 -	- -	-
175	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263](SCR),MULTI STATE	04/2008	184.26 -	- -	-
176	BHADRACHALAM-KOVVUR - [N22000264](SCR),ANDHRA PRADESH	04/2012	923.23 -	- -	-
177	GUDUR-DURGARAJPATNAM - [N22000265](SCR),ANDHRA PRADESH	04/2011	283.54 -	- -	-
178	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	289.79 -	- -	-
179	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	159.20 -	- -	-
180	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
181	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-
182	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-
183	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-
184	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	-
185	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-
186	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-
187	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	- -	-
188	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-
189	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-
190	CUMBUM-PRODDATUR - [N22000282](SCR),ANDHRA PRADESH	04/2013	829.00 -	- -	-
191	MUDKHED-PARBHANI - [N22000283](SCR),MAHARASHTRA	04/2011	390.60 -	- -	-
192	AKKANAPET-MEDAK - [N22000285](SCR),ANDHRA PRADESH	04/2012	153.00 -	- -	-
193	NADIKUDE-SRI KALAHASTI - [N22000286](SCR),ANDHRA PRADESH	04/2011	1,313.48 -	- -	-
194	BHADRACHALAM ROAD-SATTUPALLI - [N22000287](SCR),ANDHRA PRADESH	04/2010	337.49 -	- -	-
195	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288](SCR),MULTI STATE	04/2008	2,050.00 -	- -	-
196	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
197	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	165.65 -	- -	-
198	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-
199	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-
200	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-
201	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-
202	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-
203	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	- -	-
204	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	- -	-
205	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
206	MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-
207	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	01/1999 -	-
208	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,ANDHRA PRADESH	04/2007	313.24 -	01/1999 -	-
209	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-
210	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	01/1999 -	-
211	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-
212	VIRAMGAM-BHILD(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 -	- 03/2010	-
213	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	353.08 514.68	- -	-
214	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	37.68 450.00	07/2012 -	-
215	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	- -	-
216	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	491.19 2,957.21	07/2005 -	-
217	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,MULTI STATE	09/1998	925.00 -	05/2008 03/2011	-
218	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	233.00 501.69	03/2012 08/2012	-
219	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	78.23 162.87	- -	-
220	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 100.00	- -	-
221	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 1,047.00	- -	-
222	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	02/1999	138.00 901.62	- -	-
223	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	324.66 528.65	- -	-
224	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	104.79 -	- -	-
225	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	727.13 727.13	- -	-
226	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	726.96 810.78	- -	-
227	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,ANDHRA PRADESH	04/2006	378.56 671.82	- -	-
228	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 404.19	- -	-
229	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 125.00	- -	-
230	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 456.00	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
231	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NEFR,BIHAR	09/2006	300.00 300.00	- -	-
232	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-
233	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	-
234	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-
235	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-
236	DELHI-SOHNANUHIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-
237	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-
238	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64 -	- -	-
	Total		95,622.58 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
239	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,ANDHRA PRADESH	02/2010	390.56 -	02/2012 -	06/2013
240	2 LANING OF MUZAFFARPUR - SONBARSA - [N24000174]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	11/2013
241	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 157.47	09/2007 03/2014	12/2013
242	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	12/2013 -	12/2013
243	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	12/2013
244	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	01/2014
245	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	01/2014 -	01/2014
246	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	01/2014 -	01/2014
247	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	01/2014 -	01/2014
248	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	01/2014
249	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	02/2014 -	02/2014
250	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	02/2014 -	02/2014
251	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	02/2014 -	02/2014
252	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	09/2008 -	-
253	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	06/2005 -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
254	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,JAMMU AND KASHMIR	12/2003	166.27 -	03/2008 -	-
255	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	10/2008 -	-
256	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	06/2008 -	-
257	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	06/2008 -	-
258	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	09/2008 -	-
259	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	10/2008 -	-
260	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	10/2008 -	-
261	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	07/2008 -	-
262	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-
263	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	06/2008 -	-
264	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-
265	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	02/2010 -	-
266	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-
267	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 385.15	09/2007 07/2011	-
268	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	02/2010 -	-
269	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	09/2010 -	-
270	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	07/2012 -	-
271	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	09/2012 -	-
272	PUNE-SHOLAPUR,PKG1 - [N24000127]NHAI,MAHARASHTRA	11/2009	1,110.00 -	05/2012 -	-
273	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	05/2012 -	-
274	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	10/2011 -	-
275	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	10/2011 -	-
276	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	-
277	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	12/2012 -	-
278	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
279	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI, KARNATAKA	09/2010	946.00 -	- -	-
280	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI, TAMIL NADU	09/2010	1,655.00 -	09/2013 -	-
281	TALEGAON-AMRAVATI - [N24000140]NHAI, MAHARASHTRA	11/2009	567.00 -	11/2013 -	-
282	HAZARIBAGH-RANCHI - [N24000141]NHAI, JHARKHAND	08/2010	625.07 -	01/2013 -	-
283	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, TAMIL NADU	09/2010	852.00 -	03/2013 -	-
284	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	-
285	AMRITSAR-PATHANKOT - [N24000147]NHAI, PUNJAB	05/2010	705.00 -	11/2012 -	-
286	DEOLI-KOTA - [N24000148]NHAI, RAJASTHAN	01/2011	593.00 -	07/2013 -	-
287	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI, KERALA	02/2010	617.00 -	08/2012 -	-
288	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI, MAHARASHTRA	02/2011	193.45 -	11/2012 -	-
289	DEVIHALLI-HASSAN - [N24000152]NHAI, KARNATAKA	12/2010	453.00 -	- -	-
290	MURADABAD-BAREILY - [N24000154]NHAI, UTTAR PRADESH	04/2010	1,267.00 -	06/2013 -	-
291	PUNE-SATARA(NH-4) - [N24000156]NHAI, MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	-
292	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI, KARNATAKA	03/2011	839.00 -	- -	-
293	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI, KARNATAKA	12/2010	480.00 -	- -	-
294	INDORE-DEWAS(NH-3) - [N24000159]NHAI, MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-
295	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-
296	PATNA-MUZZAFFARPUR - [N24000165]NHAI, BIHAR	08/2010	671.30 -	02/2013 -	-
297	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, BIHAR	05/2011	351.54 -	05/2013 -	-
298	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI, GUJARAT	12/2010	1,008.50 -	06/2013 -	-
299	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI, GUJARAT	03/2011	785.50 -	08/2013 -	-
300	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI-ENNORE PORT CONNECTIVITY - [N24000173]NHAI, TAMIL NADU	06/2011	600.00 -	06/2013 -	-
301	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT	01/2011	953.88 -	07/2013 -	-
302	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI, TAMIL NADU	05/2010	374.00 -	05/2013 -	-
303	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI, TAMIL NADU	09/2011	485.00 -	08/2013 -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
304	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,TAMIL NADU	04/2011	571.00 -	10/2013 -	-
305	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	03/2013 -	-
306	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	-
307	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	-
308	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	-
309	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	01/2013 -	-
310	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	08/2013 -	-
311	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	02/2013 -	-
312	BAREILY-SITAPUR - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	-
313	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	-
314	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	08/2013 -	-
315	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	08/2013 -	-
316	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	08/2013 -	-
317	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	07/2012 -	-
318	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	- -	-
319	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,KARNATAKA	11/2010	680.00 -	- -	-
	Total		52,568.57 -		
	<u>SHIPPING AND PORTS</u>				
320	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,ODISHA	12/2005	154.84 253.36	- 01/2009	12/2010
321	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 298.17	04/2009 11/2009	02/2011
322	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY VESSELS - [N25000014]SHIPP.,MAHARASHTRA	10/2007	359.44 -	04/2011 11/2011	11/2011
323	MODIFICATION & STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST,GUJARAT	06/2010	277.00 -	03/2012 -	03/2012
324	ACQUISITION OF TWO NOS. OF 3060 DWT - [N25000043]SHIPP.,MAHARASHTRA	04/2009	277.03 280.00	12/2011 10/2012	10/2012
325	MECHANIZATION OF COAL HANDLING FACILITIES TO 200000 DWT VESSELS ON DBFOT BASIS - [N25000049]PORT TRUST,ANDHRA PRADESH	02/2010	444.10 -	06/2010 -	11/2012

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
326	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST - [N25000037]PORT TRUST,GUJARAT	04/2005	882.00 -	02/2011 -	12/2012
327	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,GUJARAT	12/2005	702.00 -	03/2011 -	03/2013
328	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST,GUJARAT	02/2011	830.00 -	05/2013 -	05/2013
329	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,MULTI STATE	07/2011	220.49 -	01/2013 06/2013	06/2013
330	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN - [N25000048]PORT TRUST,KERALA	03/2009	3,500.00 4,150.00	01/2012 09/2012	08/2013
331	ACQUISITION OF 4 NOS OF 82000 DWT KAMSAVMAX BULK CARRIERS FROM M/S JIANGSU EASTERN HEAVY INDUSTRIES - [N25000051]SHIPP.,MAHARASHTRA	08/2010	612.72 532.83	12/2012 11/2013	11/2013
332	ACQUISITION OF THREE(3) NOS OF 6500TEU CELLULAR CONTAINER VESSELS FROM M/S STX SHIPBUILDING CO. LTD. - [N25000052]SHIPP.,MAHARASHTRA	10/2010	1,028.10 1,012.23	12/2013 11/2013	11/2013
333	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 11/2010	-
334	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL - [N25000003]PORT TRUST,MAHARASHTRA	10/2005	800.00 1,571.60	10/2008 -	-
	Total		12,760.79 -		
	<u>TELECOMMUNICATIONS</u>				
335	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) PH-5.1 PUNJAB - [N26000041]BSNL,PUNJAB	02/2008	373.94 -	12/2008 -	12/2012
336	GSM EQUIPMENT OF 799000LINES (2G) 101000 LINES 3(G) JHARKHANDPHASE V.1 TELECOM CIRCLE - [N26000088]BSNL,JHARKHAND	03/2008	328.13 -	03/2009 -	01/2013
337	GSM EQUIPMENT OF 1625000LINES (2G) 325000 LINES 3(G) MP PHASE V.1 TELECOM CIRCLE - [N26000090]BSNL,MADHYA PRADESH	11/2009	916.70 -	11/2010 12/2012	09/2013
338	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK.PROCUREMENT OF GPON EQUIPMANT - [N26000072]BSNL,MULTI STATE	12/2007	952.88 -	03/2010 -	-
339	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK,PROCUREMENT OF GEON EQUIPMENT - [N26000073]BSNL,MULTI STATE	12/2007	152.65 -	03/2010 -	-
340	GSM EQUIPMENT OF 200000LINES (2G) UP(WEST)PHASE V.2 TELECOM CIRCLE - [N26000082]BSNL,UTTAR PRADESH	10/2008	336.84 -	10/2009 -	-
	Total		3,061.14 -		
	<u>URBAN DEVELOPMENT</u>				
341	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA	05/2006	6,395.00 -	06/2011 -	03/2013
342	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI - [N28000048]CPWD,MAHARASHTRA	11/2006	114.18 173.08	04/2009 -	-
	Total		6,509.18 -		

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>WATER RESOURCES</u>				
343	PAGLADIYA DAM PROJECT - [300100001]MOWR,ASSAM	01/2001	542.90 -	12/2007 -	12/2012
	Total		542.90 -		
	Grand Total		215,338.23		

List of On Schedule Projects w.r.t. Original Schedule

(March 2014)							
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
1	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]	2/2011	452.00 -	452.00	230.42	03/2015 -	03/2015
2	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]	10/2012	217.60 -	217.60	0.04	03/2015 -	03/2015
	Total		669.60 -	669.60	230.46		
	<u>COAL</u>						
3	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]	6/2011	746.04 -	535.10	222.53	03/2015 -	03/2015
4	BINA EXTN. PROJ(6.0 MTPA) - [N06000019]	11/2006	168.97 -	168.97	44.08	03/2014 -	03/2014
5	GOPAL PRASAD OCP (15MTY) - [N06000042]	2/2008	395.87 -	395.87	75.42	03/2015 -	03/2015
6	PELMA OCP(10.00MTY) - [N06000045]	7/2008	448.32 -	448.32	-	03/2015 -	03/2015
7	RKP OCP PHASE-I - [N06000079]	3/2010	209.78 -	209.78	93.46	03/2015 -	03/2015
8	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]	12/2009	510.85 -	510.85	268.01	03/2016 -	03/2016
9	KISTARAM OCP - [N06000089]	11/2010	242.29 -	242.29	-	03/2015 -	03/2015
10	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.14 -	430.14	65.48	03/2016 -	03/2016
11	KALYANIKHANI OPENCAST PROJECT - [N06000101]	7/2012	417.33 -	417.33	0.24	07/2016 -	07/2016
12	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]	6/2012	365.01 -	365.01	5.43	06/2015 -	06/2015
13	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]	4/2012	258.56 -	258.56	55.25	03/2016 -	03/2016
14	MOONIDIH XV SEAM UG - [N06000098]	8/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015
15	MURAI DIH UG TURN-KEY PROJECT - [N06000096]	2/2011	339.88 -	339.88	-	04/2014 -	04/2014
16	JALAGAM VENGALA RAO OCP-II - [N06000094]	7/2011	447.06 -	447.06	29.04	03/2015 -	03/2015
17	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	7/2011	162.76 -	162.76	2.56	03/2015 -	03/2015
18	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	19.19	03/2018 -	03/2018
19	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.33 -	610.33	-	03/2022 -	03/2022
20	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	67.22	03/2020 -	03/2020

(March 2014)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
21	KARMA OCP (1.0MTY) - [N06000088]	6/2009	162.46 -	162.46	55.85	03/2014 -	03/2014
22	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	90.43	03/2016 -	03/2016
23	BATURA OCP (2.0 MTY) - [N06000049]	9/2008	203.82 -	203.82	-	03/2015 -	03/2015
24	TALABIRA OCP - [N06000043]	3/2008	447.72 -	447.72	50.46	03/2016 -	03/2016
25	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.00 -	490.10	160.06	03/2017 -	03/2017
26	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]	12/2009	1,352.04 -	1,143.54	613.44	03/2016 03/2016	03/2016
	Total		11,779.48 -	11,408.14	1,918.15		
	<u>PETROLEUM</u>						
27	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	522.90	03/2015 -	03/2015
28	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]	3/2012	5,608.40 -	5,608.40	2,182.76	05/2015 -	05/2015
29	REWARI KANPUR PIPELINE PROJECT - [N16000145]	2/2012	1,210.64 -	1,210.64	504.90	11/2015 -	11/2015
30	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	11/2012	666.00 -	701.00	202.33	11/2015 -	11/2015
31	PIPELINE REPLACEMENT PROJECT-3 - [N16000137]	4/2012	2,547.26 -	2,547.26	1,015.93	05/2014 -	05/2014
32	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]	4/2012	600.17 -	600.17	219.43	12/2014 -	12/2014
33	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]	2/2011	913.00 -	913.00	106.53	07/2015 -	07/2015
34	MOUNDED BULLET PROJECT AT CPCL - [N16000154]	12/2012	279.00 -	279.00	65.09	12/2014 -	12/2014
35	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]	4/2013	284.82 -	284.82	-	04/2015 -	04/2015
36	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	5/2013	4,124.35 -	4,124.35	-	04/2016 -	04/2016
37	KOTA JOBNER PIPELINE PROJECT - [N16000170]	4/2011	276.26 -	276.26	135.34	03/2015 -	03/2015
38	MARKETING TERMINAL AT PARADEEP - [N16000168]	7/2009	199.75 -	199.75	133.42	06/2014 -	06/2014
39	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]	3/2013	1,138.50 -	1,138.50	33.92	04/2015 -	04/2015
40	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]	12/2012	3,513.07 -	3,513.07	-	02/2016 -	02/2016
41	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]	9/2011	202.25 -	202.25	33.26	07/2016 -	07/2016
42	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]	8/2011	586.00 -	586.00	160.16	08/2015 -	08/2015
43	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	9/2012	871.35 -	871.35	10.93	03/2015 -	03/2015

(March 2014)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		25,080.45	25,721.47	5,326.90		
	<u>POWER</u>						
44	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]	3/2011	2,569.25	2,569.25	-	03/2014	03/2014
45	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]	5/2011	1,961.87	1,961.87	-	05/2014	05/2014
46	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33	297.33	214.02	08/2014	08/2014
47	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]	1/2012	1,422.85	1,422.85	633.79	01/2015	01/2015
48	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]	11/2011	2,127.51	2,127.51	-	07/2014	07/2014
49	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATNAM OF ANDHRA PRADESH(PGCIL) - [N18000111]	8/2011	1,637.34	1,637.34	1,353.68	08/2014	08/2014
50	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]	2/2012	1,310.85	1,310.85	-	02/2015	02/2015
51	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]	2/2012	1,927.16	1,927.16	906.91	10/2014	10/2014
52	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]	6/2012	1,909.24	1,909.24	381.51	06/2015	06/2015
53	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]	3/2013	2,514.88	2,514.88	23.38	12/2015	12/2015
54	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	3/2013	514.20	514.20	-	06/2015	06/2015
55	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	7/2012	1,527.00	1,527.00	64.00	08/2017	08/2017
56	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	11/2012	11,846.00	11,846.00	1,321.00	05/2017	05/2017
57	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139]	1/2013	182.80	182.80	10.71	10/2014	10/2014
58	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]	12/2012	156.04	156.04	24.39	10/2014	10/2014
59	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]	9/2012	803.34	803.34	211.42	03/2015	03/2015
60	VINDHYACHAL STPP STAGE-V - [N18000134]	12/2011	3,180.40	3,180.40	881.00	08/2015	08/2015
61	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]	2/2014	243.53	243.53	-	08/2014	08/2014
62	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	2/2014	908.08	908.08	-	06/2016	06/2016

(March 2014)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
63	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]	2/2014	539.82 -	539.82	-	06/2016 -	06/2016
64	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]	1/2014	374.63 -	374.63	-	04/2016 -	04/2016
65	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,364.52	-	05/2016 -	05/2016
66	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154]	10/2013	1,315.90 -	1,315.90	-	11/2016 -	11/2016
67	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]	9/2013	1,575.30 -	1,575.30	-	05/2016 -	05/2016
68	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]	9/2013	680.69 -	680.69	-	03/2016 -	03/2016
69	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	2/2013	11,638.55 -	11,638.55	1,030.00	09/2017 -	09/2017
70	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]	2/2014	167.40 -	167.40	-	12/2015 -	12/2015
71	SOLAPUR STPP - [N18000133]	3/2012	9,395.18 -	9,395.18	2,085.00	11/2016 -	11/2016
72	MOUDA STPP STAGE 2 - [N18000132]	3/2012	7,921.47 -	7,921.47	1,878.00	09/2016 -	09/2016
73	KUDGI STPP STAGE 1 - [N18000131]	12/2011	15,166.19 -	15,166.19	3,237.00	12/2016 -	12/2016
74	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]	6/2012	1,263.26 -	1,263.26	598.85	11/2014 -	11/2014
75	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]	11/2011	723.63 -	723.63	314.55	11/2014 -	11/2014
76	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]	12/2011	901.77 -	901.77	598.30	08/2014 -	08/2014
77	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]	3/2012	206.44 -	206.44	42.57	06/2014 -	06/2014
78	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]	3/2012	198.63 -	198.63	-	09/2014 -	09/2014
79	TRANSMISSION SYS ASSOCIATED WITH KRISHNAPATNAM UMP-PART C1 - [N18000121]	2/2012	324.33 -	324.33	141.27	08/2014 -	08/2014
	Total		90,797.38 -	90,797.38	15,951.35		
	<u>RAILWAYS</u>						
80	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	4/1998	183.23 -	818.29	111.78	02/2015 -	02/2015
81	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]	4/2008	829.74 -	829.74	53.05	03/2015 -	03/2015
82	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	4/2010	2,619.02 -	2,913.51	398.86	03/2016 -	03/2016
83	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	4/2010	3,951.98 -	3,951.98	308.18	03/2016 -	03/2016

(March 2014)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
84	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	4/2008	653.19 -	653.47	277.38	03/2014 -	03/2014
85	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]	4/2008	1,389.62 -	1,389.62	796.60	03/2014 -	03/2014
86	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	1,176.09 -	3,845.60	1.92	02/2020 -	02/2020
87	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	4/2010	423.66 -	423.66	158.41	03/2017 -	03/2017
88	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]	4/2009	257.42 -	257.42	34.36	03/2014 -	03/2014
89	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	4/2011	299.60 -	299.60	1.10	03/2017 -	03/2017
90	PLASSEY-JIAGANJ DOUBLING - [N22000220]	4/2011	248.07 -	248.07	12.05	03/2015 -	03/2015
91	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	4/2010	309.44 -	388.67	74.58	12/2015 -	12/2015
92	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]	4/2010	622.41 -	2,030.50	1.60	02/2019 -	02/2019
93	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	3/2013	4,874.58 -	4,874.58	-	03/2016 -	03/2016
94	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]	4/2008	516.23 -	516.23	478.66	03/2014 -	03/2014
	Total		18,354.28 -	23,440.94	2,708.53		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
95	PANIPAT-ROHTAK - [N24000151]	4/2011	807.00 -	807.00	1,325.75	10/2014 -	10/2014
96	4 LANNING OF NAGPUR-BETUL - [N24000155]	2/2011	2,498.76 -	2,498.76	2,425.10	08/2014 -	08/2014
97	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]	9/2011	2,848.00 -	2,848.00	993.84	03/2014 -	03/2014
98	NASHRI CHANANI - [N24000162]	6/2010	2,159.00 -	2,159.00	374.22	06/2015 -	06/2015
99	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]	7/2010	1,987.00 -	1,987.00	1,080.00	07/2015 -	07/2015
100	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]	11/2011	1,535.00 -	1,535.00	1,328.51	05/2014 -	05/2014
101	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]	10/2011	375.09 -	375.09	174.34	04/2014 -	04/2014
102	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]	11/2011	909.00 -	909.00	959.15	05/2014 -	05/2014
103	BARSAT-KRISHNANAGAR - [N24000229]	8/2012	867.00 -	867.00	598.56	02/2015 -	02/2015
104	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]	6/2013	1,287.95 -	1,287.95	52.18	11/2015 -	11/2015
105	REENGUS SIKAR - [N24000227]	3/2012	333.51 -	333.51	260.16	09/2014 -	09/2014
106	RANCHI-RARGA-JAMSETHPUR - [N24000215]	12/2012	1,479.00 -	1,479.00	285.46	06/2015 -	06/2015

(March 2014)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
107	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]	4/2012	624.00 -	624.00	424.10	04/2014 -	04/2014
108	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]	7/2012	356.40 -	356.40	42.51	07/2014 -	07/2014
109	NAGPUR-WAINGANGA BRIDGE - [N24000210]	4/2012	484.19 -	484.19	283.53	10/2014 -	10/2014
110	KRISHNANAGAR-BERHAMPUR - [N24000209]	2/2012	702.16 -	702.16	651.04	07/2014 -	07/2014
111	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]	4/2012	1,396.18 -	1,396.18	1,383.05	09/2014 -	09/2014
112	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]	12/2011	1,047.00 -	1,047.00	234.03	06/2014 -	06/2014
113	BEAWAR-PALI-PINDWARA - [N24000199]	12/2011	2,388.00 -	2,388.00	1,846.87	06/2014 -	06/2014
114	PANIKHOLI-RIMOLI - [N24000197]	3/2012	1,410.00 -	1,410.00	158.91	09/2014 -	09/2014
115	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]	10/2011	1,565.00 -	1,565.00	1,119.27	10/2014 -	10/2014
116	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]	3/2012	828.00 -	828.00	582.60	09/2014 -	09/2014
117	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	1,928.22	428.98	04/2015 -	04/2015
118	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	61.44	12/2015 -	12/2015
119	2 LANING WITH PS KANPUR KABRAI - [N24000221]	1/2013	373.47 -	373.47	43.77	07/2014 -	07/2014
120	2 LANING WITH PS AGRA ALIGARH - [N24000220]	10/2012	250.50 -	250.50	328.56	10/2014 -	10/2014
121	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	37.66	09/2015 -	09/2015
122	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]	2/2013	1,232.00 -	1,232.00	252.60	08/2015 -	08/2015
123	PANVEL-INDAPUR - [N24000216]	12/2011	942.69 -	942.69	264.53	06/2014 -	06/2014
124	2LANING WITH PS GOPALGANJ-CHAPPRA - [N24000190]	12/2011	325.00 -	325.00	166.73	05/2014 -	05/2014
125	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]	9/2011	574.00 -	574.00	794.16	03/2014 -	03/2014
	Total		37,211.36 -	37,211.36	18,961.61		
	<u>STEEL</u>						
126	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH - [N12000078]	7/2012	332.65 -	332.65	102.39	08/2014 -	08/2014
127	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079]	6/2012	237.09 -	254.90	31.93	12/2014 -	12/2014
128	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]	11/2012	313.05 -	339.35	83.98	06/2015 -	06/2015
129	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]	10/2012	160.48 -	160.48	18.86	09/2014 -	09/2014

(March 2014)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
130	REBUILDING OF COB-7 AT BSL - [N12000083]	10/2013	245.67 -	245.67	6.91	05/2016 -	05/2016
	Total		1,288.94 -	1,333.05	244.07		
	<u>URBAN DEVELOPMENT</u>						
131	DELHI MRTS PHASE-III - [N28000056]	9/2011	38,585.00 -	38,585.00	7,107.57	03/2016 -	03/2016
132	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]	2/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019
	Total		64,990.14 -	64,990.14	7,107.57		
	Grand Total		250,171.63	255,572.08	52,448.64		

List of Delayed Projects w.r.t. Original and Revised Schedule

(March 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00 -	17,270.00	17,198.00	12/2008 -	12/2014	72	-
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 -	5,677.00	-	09/2010 -	03/2015	54	-
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	-	12/2015 -	11/2016	11	-
4	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	-	12/2016 -	03/2017	3	-
	Total		40,442.00 -	46,726.00	17,198.00				
	<u>CIVIL AVIATION</u>								
5	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 335.61	388.53	278.32	05/2012 -	04/2014	23	-
6	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	344.28	-	03/2014 -	10/2014	7	-
7	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	309.46	269.55	01/2011 04/2013	03/2015	50	23
	Total		989.35 -	1,042.27	547.87				
	<u>COAL</u>								
8	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	471.66 341.63	341.63	119.71	03/2011 -	03/2014	36	-
9	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,UTTAR PRADESH	06/2011	789.88 -	741.62	388.56	03/2013 -	03/2014	12	-
10	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,TAMIL NADU	10/2004	2,030.78 3,027.59	3,027.59	2,904.44	06/2009 -	06/2014	60	-
11	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	5,191.62	03/2012 -	08/2014	29	-
12	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,ANDHRA PRADESH	12/2009	212.34 1,228.39	1,228.39	1,206.66	03/2013 09/2012	03/2015	24	30
13	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 -	259.40	6.99	03/2012 -	03/2015	36	-
14	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	116.72	03/2013 -	03/2015	24	-
15	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.63 -	479.63	120.15	03/2013 -	03/2015	24	-
16	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,ANDHRA PRADESH	12/2009	418.97 -	418.97	240.26	03/2012 -	03/2015	36	-
17	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,ANDHRA PRADESH	03/2010	181.19 -	181.19	35.35	03/2012 -	03/2015	36	-

(March 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
18	PUANADH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	123.07	03/2013 -	03/2015	24	-
19	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,632.11	03/2014 -	03/2016	24	-
20	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,345.03	03/2014 -	03/2016	24	-
21	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	469.78 -	706.40	32.17	07/2012 -	03/2016	44	-
22	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	131.62	03/2010 -	03/2016	72	-
23	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35 -	462.35	270.85	03/2014 -	03/2016	24	-
24	KAKATIYA LONGWALL - [N06000048]SCCL,ANDHRA PRADESH	12/2008	453.63 -	453.63	102.23	12/2012 -	03/2016	39	-
25	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	33.46	03/2014 -	03/2016	24	-
26	PENGANGA OC - [N06000066]WCL,MAHARASHTRA	10/2008	339.77 -	339.77	2.30	03/2014 -	03/2016	24	-
27	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	126.88	03/2012 -	03/2016	48	-
28	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24	-
29	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.42 -	321.50	213.59	03/2014 -	03/2016	24	-
30	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	35.38	03/2011 -	03/2016	60	-
31	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	141.89	03/2012 -	03/2016	48	-
32	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	118.59	03/2010 -	03/2017	84	-
33	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL	11/2006	287.18 -	287.17	36.31	03/2011 -	03/2017	72	-
34	JAGANNATHPOR OC - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	152.43	-	03/2015 -	03/2017	24	-
35	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	63.66	03/2012 -	03/2017	60	-
36	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 -	5,907.11	339.15	12/2015 -	04/2018	28	-
37	KUSMUNDA EXPN.OCP(SECL)(10-15)MTY - [N06000008]SECL,CHHATISGARH	06/2008	1,188.31 7,612.33	7,612.33	747.82	03/2013 03/2023	03/2023	120	0
	Total		26,241.09 -	36,434.57	15,826.57				
	STEEL								
38	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,JHARKHAND	05/2010	6,325.00 -	6,325.00	4,591.34	12/2011 -	03/2014	27	-
39	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,ANDHRA PRADESH	06/2006	108.00 216.68	216.68	160.46	09/2008 12/2013	04/2014	67	4
40	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,WEST BENGAL	06/2008	14,443.00 -	16,408.00	15,787.87	12/2011 -	06/2014	30	-

(March 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
41	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL,ANDHRA PRADESH	10/2005	8,692.00 12,291.00	12,291.00	10,792.31	10/2009 10/2012	07/2014	57	21
42	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]RINL,MULTI STATE	07/2007	480.00 -	450.00	309.45	09/2009 05/2012	07/2014	58	26
43	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA	12/2011	187.33 -	187.33	119.88	10/2013 -	08/2014	10	-
44	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]SAIL,ODISHA	08/2010	11,812.00 -	11,812.00	10,870.17	03/2013 -	09/2014	18	-
45	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,KARNATAKA	04/2011	572.00 -	572.00	379.62	04/2013 09/2014	09/2014	17	0
46	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,WEST BENGAL	08/2010	2,875.00 -	2,875.00	2,153.22	12/2012 -	12/2014	24	-
47	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]NMDC,CHHATISGARH	01/2007	295.89 607.17	607.17	369.58	12/2011 01/2015	01/2015	37	0
48	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,KARNATAKA	02/2011	898.55 -	898.55	291.82	05/2013 01/2015	01/2015	20	0
49	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	12,491.86	03/2013 -	03/2015	24	-
50	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL,ODISHA	11/2011	254.55 -	254.55	104.16	11/2013 -	06/2015	19	-
	Total		64,208.32 -	70,162.28	58,421.74				
	<u>PETROLEUM</u>								
51	WAX PROJECT - [N16000101]NRL,ASSAM	06/2010	576.60 -	676.05	511.99	12/2013 -	03/2014	3	-
52	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,MAHARASHTRA	06/2007	3,248.78 5,633.44	5,633.44	5,190.51	08/2010 03/2012	05/2014	45	26
53	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,MAHARASHTRA	10/2007	5,713.03 8,813.41	8,813.41	7,351.12	05/2010 03/2013	05/2014	48	14
54	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,MAHARASHTRA	06/2007	1,436.21 1,456.96	1,456.96	1,100.32	07/2010 05/2012	05/2014	46	24
55	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,MAHARASHTRA	01/2009	7,133.39 -	7,133.39	5,543.40	09/2012 -	05/2014	20	-
56	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,MULTI STATE	01/2010	2,163.64 2,331.62	2,331.62	1,889.99	06/2012 -	05/2014	23	-
57	FIRE WATER NETWORK AT URAN - [N16000141]ONGC,MAHARASHTRA	05/2010	171.68 -	171.68	96.43	06/2013 -	05/2014	11	-
58	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]ONGC,TRIPURA	07/2008	288.04 288.04	253.66	210.07	08/2012 -	06/2014	22	-
59	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,MULTI STATE	08/2010	8,140.00 -	8,140.00	6,422.66	02/2014 -	06/2014	4	-
60	POLYPROPYLENE UNIT - [N16000113]MANGALORE REFIN,KARNATAKA	05/2009	1,803.78 -	1,803.78	884.59	07/2012 -	06/2014	23	-
61	MRPL PHASE-III EXPANSION - [N16000114]MANGALORE REFIN,KARNATAKA	08/2008	12,412.00 -	12,160.26	11,518.36	01/2012 -	06/2014	29	-

(March 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
62	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 -	861.79	495.39	05/2013 06/2014	06/2014	13	0
63	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]BPCL,MAHARASHTRA	08/2009	246.81 -	276.83	258.57	04/2012 -	06/2014	26	-
64	GAS TURBINE GENERATION SET - [N18000146]OIL,ASSAM	07/2009	216.88 -	216.88	177.92	10/2011 -	06/2014	32	-
65	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,ASSAM	08/2008	144.02 -	204.29	154.08	06/2012 -	06/2014	24	-
66	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,ANDHRA PRADESH	03/2009	3,597.00 2,730.00	2,730.00	2,061.74	09/2011 03/2012	07/2014	34	28
67	102 MW WIND POWER PROJECT - [N16000119]ONGC,RAJASTHAN	07/2010	1,106.00 -	678.02	77.45	06/2012 -	07/2014	25	-
68	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,MAHARASHTRA	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	09/2014	69	17
69	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC,MULTI STATE	11/2010	331.20 -	331.20	164.19	08/2013 -	09/2014	13	-
70	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPR,ANDHRA PRADESH	01/2006	672.00 1,038.00	1,038.00	936.55	10/2011 -	09/2014	35	-
71	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]ONGC,MULTI STATE	03/2010	3,241.03 5,916.65	6,638.94	1,451.42	03/2013 11/2014	11/2014	20	0
72	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,HARYANA	11/2007	281.07 -	281.07	4.42	10/2010 -	12/2014	50	-
73	PARADIP REFINERY PROJECT - [N16000058]IOCL,ODISHA	02/2009	29,777.00 -	32,710.00	25,230.00	11/2012 -	12/2014	25	-
74	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,MAHARASHTRA	03/2009	3,284.00 2,174.00	2,174.00	1,881.89	09/2011 05/2012	12/2014	39	31
75	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	736.65	448.92	09/2011 -	12/2014	39	-
76	CONSTRUCTION OF SIX EFFLUENT TREATMENT PLANTS (ETP), AHMEDABAD AND ANKLESWAR - [N16000099]ONGC,GUJARAT	03/2009	234.78 234.78	317.64	102.78	09/2012 -	12/2014	27	-
77	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	302.26 -	240.95	102.78	09/2012 -	12/2014	27	-
78	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE	01/2012	352.49 -	352.49	84.56	03/2014 -	12/2014	9	-
79	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 -	202.94	2.00	01/2014 -	01/2015	12	-
80	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 -	2,378.89	1,496.19	03/2013 03/2014	03/2015	24	12
81	CONSTRUCTION OF ONE ETP AT GGS-NADA, ANKLESHWAR - [N16000134]ONGC,GUJARAT	10/2011	200.69 -	200.69	8.08	07/2014 -	03/2015	8	-
82	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL,MAHARASHTRA	01/1999	1,419.00 -	1,419.00	409.10	12/2014 -	03/2015	3	-
83	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 -	2,592.17	234.78	05/2014 -	05/2015	12	-
84	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPR,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	793.29	10/2011 -	06/2015	44	-
85	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPR,KERALA	01/2006	993.00 1,693.00	1,693.00	1,102.03	01/2012 -	06/2015	41	-

(March 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
86	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	961.93	09/2012 -	08/2015	35	-
87	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	11/2012	309.81 -	309.82	67.83	10/2014 -	10/2015	12	-
88	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	270.00	-	12/2014 -	10/2015	10	-
89	CONSTRUCTION OF THREE ETPS, MEHSANA - [N16000135]ONGC,GUJARAT	03/2012	260.74 -	260.74	0.52	11/2014 -	11/2015	12	-
90	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,MAHARASHTRA	01/2007	2,323.40 2,920.82	2,920.82	1,915.45	09/2010 03/2012	12/2015	63	45
91	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18 -	7,596.18	13.50	01/2013 -	12/2015	35	-
92	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE	06/2010	2,523.00 -	2,523.00	1,002.33	01/2014 -	12/2015	23	-
93	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	330.47	270.05	03/2012 -	03/2016	48	-
94	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL,KERALA	01/1999	14,225.00 -	14,225.00	1,814.37	12/2015 -	05/2016	5	-
95	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,MULTI STATE	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	06/2016	122	48
96	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	723.64	-	03/2013 -	06/2016	39	-
97	AHMEDABAD REDEVELOPMENT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10 -	1,916.10	784.46	12/2014 -	12/2016	24	-
98	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63 -	2,189.63	1,039.42	12/2014 -	12/2016	24	-
99	MEHESANA REDEVELOPMENT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	3,823.00	1,076.07	04/2015 -	03/2017	23	-
100	CREATION OF SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND ETP AT MADHUBAN - [N16000167]OIL,MULTI STATE	08/2006	374.56 -	374.56	10.60	09/2012 -	03/2017	54	-
	Total		139,493.44 -	153,758.67	92,059.01				
	<u>POWER</u>								
101	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]PGCIL,MULTI STATE	08/2008	2,360.95 -	2,580.90	-	08/2012 -	03/2014	19	-
102	765 KV POOLING STATION AND NETWORK WITH DVC AND MAITHON RBC - [N18000069]PGCIL,MULTI STATE	08/2008	7,075.33 -	7,075.33	-	08/2012 -	03/2014	19	-
103	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 -	2,074.86	-	03/2013 -	03/2014	12	-
104	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19 -	2,743.19	-	12/2013 -	03/2014	3	-
105	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 -	752.64	-	07/2013 -	03/2014	8	-

(March 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
106	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	633.83	11/2012 -	04/2014	17	-
107	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 -	477.69	471.52	09/2010 -	06/2014	45	-
108	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]PGCIL,MULTI STATE	09/2011	1,366.34 -	1,366.34	952.26	12/2013 -	06/2014	6	-
109	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	393.96	02/2014 -	06/2014	4	-
110	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL,MADHYA PRADESH	03/2012	213.78 -	213.78	103.39	03/2014 -	06/2014	3	-
111	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,HIMACHAL PRADESH	10/2005	2,304.56 -	2,716.00	2,349.46	10/2010 -	08/2014	46	-
112	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	487.49	277.05	06/2014 -	09/2014	3	-
113	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 623.44	951.48	745.55	07/2013 -	11/2014	16	-
114	SYSTEM STRENGTHENING IN NR FOR SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	975.26	08/2012 -	12/2014	28	-
115	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,007.98	04/2013 -	12/2014	20	-
116	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,272.71	09/2014 -	12/2014	3	-
117	BARH STPP STAGE -II - [N18000047]NTPC,BIHAR	02/2008	7,341.04 -	7,341.04	6,847.00	08/2013 -	03/2015	19	-
118	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	3,739.68	10/2012 -	03/2015	29	-
119	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. - [N18000076]PGCIL,MULTI STATE	03/2010	4,672.99 -	4,672.99	2,964.78	11/2012 -	03/2015	28	-
120	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	241.16	11/2013 -	03/2015	16	-
121	KOLDAM HEP (NTPC) - [180100211]NTPC,HIMACHAL PRADESH	10/2002	4,527.15 7,220.00	7,220.00	5,687.00	04/2009 -	05/2015	73	-
122	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 -	1,746.65	317.22	08/2014 -	05/2015	9	-
123	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	-	04/2015 -	05/2015	1	-
124	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	7,937.67	08/2013 -	06/2015	22	-
125	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP & BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	1,647.80	12/2012 -	06/2015	30	-

(March 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
126	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	66.52	01/2013 -	06/2015	29	-
127	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,182.61	11/2013 -	06/2015	19	-
128	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	808.16	11/2012 -	06/2015	31	-
129	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	963.76	08/2014 -	06/2015	10	-
130	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAND AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	1,427.54	10/2014 -	06/2015	8	-
131	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC, WEST BENGAL	09/2005	1,061.38 -	1,501.75	1,482.62	09/2009 -	07/2015	70	-
132	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99 -	1,128.38	811.78	08/2013 09/2015	09/2015	25	0
133	TRANSM SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B - [N18000077]PGCIL, WEST BENGAL	04/2010	4,404.57 -	4,404.57	464.43	01/2015 -	12/2015	11	-
134	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM	01/2011	913.63 -	913.63	573.22	07/2006 12/2015	12/2015	113	0
135	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATTISGARH	03/2012	9,569.76 -	9,569.76	1,577.68	06/2015 -	12/2015	6	-
136	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC, ASSAM	01/2008	4,375.35 -	4,375.35	4,311.00	07/2011 -	08/2016	61	-
137	KISHANGANGA HEP - [N18000031]NHPC,JAMMU AND KASHMIR	07/2007	2,238.67 3,642.04	3,642.00	3,283.02	01/2016 -	11/2016	10	-
138	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,UTTAR PRADESH	07/2006	1,657.00 2,978.86	2,978.86	692.39	07/2010 02/2016	02/2017	79	12
139	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 -	4,653.95	2,816.40	12/2009 06/2016	03/2017	87	9
140	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	12/2003	8,692.97 -	8,693.00	9,238.00	12/2009 -	03/2017	87	-
141	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 -	3,846.30	2,020.00	03/2013 -	03/2017	48	-
142	PARBATI HEP (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	5,366.00	4,373.85	09/2009 -	07/2018	106	-
143	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	10,667.00	6,788.54	09/2010 -	07/2018	94	-
144	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,UTTARAKHAND	08/2008	2,491.58 -	3,745.08	479.33	07/2014 -	07/2018	48	-
	Total		124,490.44 -	142,171.58	81,926.13				
	<u>RAILWAYS</u>								
145	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	432.72	399.71	12/2009 03/2011	03/2014	51	36

(March 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
146	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 224.89	246.44	141.55	03/2012 12/2013	03/2014	24	3
147	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 482.70	482.70	560.17	03/2013 -	03/2014	12	-
148	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	146.95 -	171.02	141.84	06/2013 -	06/2014	12	-
149	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	288.00	-	02/2009 02/2009	08/2014	66	66
150	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	276.00	-	03/2009 03/2009	08/2014	65	65
151	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	09/2001	120.00 245.39	245.39	225.46	12/2008 -	09/2014	69	-
152	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	401.81 495.44	1,814.10	369.57	03/2004 12/2010	12/2014	129	48
153	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 194.07	596.36	371.50	06/2004 -	12/2014	126	-
154	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 2,363.00	2,363.00	1,339.96	03/2009 12/2012	12/2014	69	24
155	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 207.52	207.52	191.41	12/2012 -	12/2014	24	-
156	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,MULTI STATE	03/1984	520.00 835.04	835.04	622.92	03/1995 -	03/2015	240	-
157	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]RE,WEST BENGAL	04/1974	31.42 393.46	445.40	179.36	03/2007 03/2007	03/2015	96	96
158	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,BIHAR	09/2001	100.00 492.98	725.53	445.01	12/2010 12/2010	03/2015	51	51
159	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	495.74	264.06	06/2013 06/2013	03/2015	21	21
160	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	186.92 261.70	261.70	72.78	02/2006 -	06/2015	112	-
161	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 2,921.00	2,921.00	2,071.46	10/2007 12/2012	12/2015	98	36
162	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	800.00	-	03/2010 -	12/2015	69	-
163	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	177.38	54.89	03/2015 -	12/2015	9	-
164	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	2,298.42	64.57	03/2014 -	03/2016	24	-
165	HYDERABAD/SECUNDERABD MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II - [N22000213]MRTP,ANDHRA PRADESH	04/2012	632.68 -	816.55	17.37	04/2012 -	03/2016	47	-
166	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 1,013.74	1,074.45	457.52	06/2005 07/2011	06/2016	132	59
167	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL,WEST BENGAL	04/2010	2,397.72 -	2,397.72	78.35	03/2016 -	06/2016	3	-

(March 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
168	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	1,423.98	478.50	03/2005 12/2008	12/2016	141	96
169	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 5,300.00	6,213.84	1,509.46	03/2014 03/2016	12/2016	33	9
170	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR, MANIPUR	04/2003	727.56 727.53	4,478.17	2,023.83	03/2011 03/2014	03/2017	72	36
171	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR, UTTAR PRADESH	04/2006	325.00 325.00	1,116.53	277.91	03/2010 03/2017	03/2017	84	0
172	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR, TRIPURA	04/2008	813.34 813.34	1,141.75	545.80	03/2014 -	03/2017	36	-
173	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR, MIZORAM	04/2008	619.34 -	2,393.48	171.49	04/2014 -	03/2017	35	-
174	SEVOK RANGPO, NEFR - [N22000102]NEFR, SIKKIM	04/2008	1,339.48 -	3,380.58	82.93	12/2015 -	03/2017	15	-
175	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NEFR, NAGALAND	04/2006	850.00 850.00	850.00	9.24	03/2015 -	03/2017	24	-
176	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NEFR, ASSAM	04/1996	1,676.31 1,676.31	4,184.84	4,020.98	03/2009 -	03/2017	96	-
177	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NEFR, TRIPURA	04/1999	895.00 -	1,091.98	955.94	03/2007 -	03/2017	120	-
178	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, JAMMU AND KASHMIR	03/1995	2,500.00 2,500.00	20,000.00	8,822.50	11/2002 -	12/2017	181	-
179	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES, NEFR - [220100201]NEFR, ASSAM	09/1997	1,000.00 1,500.00	4,500.00	3,092.23	04/2008 03/2014	12/2017	116	45
180	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NEFR, MULTI STATE	04/2000	733.00 733.00	1,655.81	1,552.32	12/2008 -	03/2018	111	-
181	KATAKHAL TO BHAIRABI - [N22000126]NEFR, ASSAM	04/1998	227.90 227.90	218.36	133.58	12/2012 -	03/2018	63	-
	Total		28,589.29 -	73,021.50	31,746.17				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
182	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, HARYANA	04/2007	486.00 -	486.00	661.58	05/2010 -	03/2014	46	-
183	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI, UTTARAKHAND	11/2011	478.00 -	478.00	308.92	10/2013 -	03/2014	5	-
184	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI, KERALA	04/2011	682.00 -	682.00	307.91	10/2013 -	03/2014	5	-
185	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, ASSAM	12/2003	196.00 331.23	331.23	183.67	07/2009 -	04/2014	57	-
186	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, ASSAM	12/2003	280.00 361.00	361.00	339.45	02/2009 -	05/2014	63	-
187	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, ASSAM	12/2003	225.00 -	225.00	269.79	06/2008 05/2014	05/2014	71	0
188	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061]NHAI, ASSAM	12/2003	212.00 333.83	333.83	73.71	09/2007 -	05/2014	80	-
189	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, UTTAR PRADESH	02/2011	1,141.00 1,141.00	1,141.00	1,319.54	08/2013 06/2014	06/2014	10	0

(March 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
190	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, ASSAM	12/2003	160.00 -	160.00	209.92	05/2008 07/2014	07/2014	74	0
191	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANNING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI, KARNATAKA	03/2011	359.00 -	359.00	39.49	09/2013 -	07/2014	10	-
192	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, ASSAM	12/2003	199.81 382.02	382.02	107.55	04/2009 12/2014	12/2014	68	0
193	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, ASSAM	12/2003	167.64 265.53	265.63	92.14	11/2008 12/2014	12/2014	73	0
194	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, ASSAM	12/2003	155.04 241.28	241.28	151.77	11/2008 12/2014	12/2014	73	0
195	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, ASSAM	12/2003	200.00 247.43	247.43	180.36	04/2009 12/2014	12/2014	68	0
196	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, ASSAM	12/2003	175.96 -	175.96	249.37	04/2008 01/2015	01/2015	81	0
197	SONAPUR TO GUWAHATI (AS-3) - [N24000044]NHAI, ASSAM	12/2003	245.00 -	245.00	491.20	03/2008 01/2015	01/2015	82	0
198	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, ASSAM	12/2003	198.16 -	198.16	306.31	04/2008 01/2015	01/2015	81	0
199	NALBARI T BIJINI (AS-7) - [N24000048]NHAI, ASSAM	12/2003	208.00 230.00	208.00	313.93	04/2008 01/2015	01/2015	81	0
200	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, ASSAM	12/2003	217.61 309.56	309.56	306.32	04/2010 01/2016	01/2016	69	0
	Total		5,986.22 -	6,830.10	5,912.93				
	<u>SHIPPING AND PORTS</u>								
201	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053]SHIPP., MAHARASHTRA	10/2010	966.46 -	994.82	427.54	02/2014 04/2014	04/2014	2	0
202	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST, TAMIL NADU	10/2002	150.00 309.00	600.00	139.80	03/2006 06/2014	06/2014	99	0
203	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY - [N25000062]SHIPP., MULTI STATE	01/2012	511.87 -	511.87	106.72	03/2014 08/2014	08/2014	5	0
204	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]MUMBAI PORT TRU, MAHARASHTRA	11/2007	1,228.00 1,460.00	2,158.16	1,004.31	12/2010 09/2012	10/2015	58	37
	Total		2,856.33 -	4,264.85	1,678.37				
	<u>TELECOMMUNICATIONS</u>								
205	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL, MULTI STATE	10/2009	384.00 -	384.00	29.45	10/2010 03/2012	03/2014	41	24
206	SUPPLY INSTALLATION TESTING AND COMMISSIONING OF RURAL WIMAX NETWORK PHASE-II - [N26000100]BSNL, MULTI STATE	07/2010	1,148.19 -	964.37	249.32	05/2011 -	05/2014	36	-

(March 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
207	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTARANCHAL - [N26000058]BSNL,UTTARAKHAND	01/2009	149.15 -	158.72	84.68	06/2009 -	06/2014	60	-
208	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL,ASSAM	06/2007	336.81 -	336.81	183.16	01/2009 -	06/2014	65	-
	Total		2,018.15 -	1,843.90	546.61				
	<u>URBAN DEVELOPMENT</u>								
209	FARIDABAD EXTENSION - [N28000057]DMRC,DELHI	09/2011	2,494.00 -	2,494.00	551.23	09/2014 -	05/2015	8	-
	Total		2,494.00 -	2,494.00	551.23				
	Grand Total		437,808.63	538,749.72	306,414.63				

List of Projects Without Milestones w.r.t. Original Schedule

			(March 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
1	D/O KAMARAJ DOMESTIC TER-PH-II AND EXP. ANNA INT. TER BLDG(K1) - [N04000038]AAI,TAMIL NADU	08/2008	1,808.00 2,015.00	01/2011 02/2012	02/2012	0/0
2	GAGAN PROJECT - [N04000065]AAI,MULTI STATE	09/2008	626.00 -	06/2013 -	06/2013	0/0
3	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 335.61	05/2012 -	04/2014	0/0
4	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	03/2014 -	10/2014	0/0
5	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	01/2011 04/2013	03/2015	0/0
6	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]AAI,CHANDIGARH	02/2011	452.00 -	03/2015 -	03/2015	0/0
7	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	03/2015 -	03/2015	0/0
	Total		4,092.95 -			0/0
	<u>COAL</u>					
8	MURAIIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	04/2014 -	04/2014	0/0
9	MOONIDH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	04/2015 -	04/2015	0/0
10	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH	12/2013	610.33 -	03/2022 -	03/2022	0/0
	Total		2,180.48 -			0/0
	<u>PETROLEUM</u>					
11	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]MANGALORE REFIN,KARNATAKA	07/2010	1,043.57 -	04/2012 -	12/2013	0/0
12	WAX PROJECT - [N16000101]NRL,ASSAM	06/2010	576.60 -	12/2013 -	03/2014	0/0
13	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,MAHARASHTRA	10/2007	5,713.03 8,813.41	05/2010 03/2013	05/2014	0/0
14	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,MAHARASHTRA	06/2007	1,436.21 1,456.96	07/2010 05/2012	05/2014	0/0
15	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,MAHARASHTRA	01/2009	7,133.39 -	09/2012 -	05/2014	0/0
16	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,MULTI STATE	01/2010	2,163.64 2,331.62	06/2012 -	05/2014	0/0
17	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,MULTI STATE	08/2010	8,140.00 -	02/2014 -	06/2014	0/0

			(March 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
18	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]BPCL,MAHARASHTRA	08/2009	246.81 -	04/2012 -	06/2014	0/0
19	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL,ODISHA	07/2009	199.75 -	06/2014 -	06/2014	0/0
20	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,ASSAM	08/2008	144.02 -	06/2012 -	06/2014	0/0
21	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,MAHARASHTRA	08/2006	3,195.16 3,690.37	12/2008 04/2013	09/2014	0/0
22	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPR,ANDHRA PRADESH	01/2006	672.00 1,038.00	10/2011 -	09/2014	0/0
23	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,HARYANA	11/2007	281.07 -	10/2010 -	12/2014	0/0
24	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	09/2011 -	12/2014	0/0
25	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	302.26 -	09/2012 -	12/2014	0/0
26	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL,TAMIL NADU	12/2012	279.00 -	12/2014 -	12/2014	0/0
27	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL,MAHARASHTRA	01/1999	1,419.00 -	12/2014 -	03/2015	0/0
28	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 -	04/2015 -	04/2015	0/0
29	SURAT PARADIP PIPELINE PROJECT - [N16000163]GAIL,MULTI STATE	10/2012	10,281.00 -	- -	04/2015	0/0
30	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC,MULTI STATE	04/2013	284.82 -	04/2015 -	04/2015	0/0
31	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPR,KARNATAKA	01/2006	732.00 1,227.00	10/2011 -	06/2015	0/0
32	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPR,KERALA	01/2006	993.00 1,693.00	01/2012 -	06/2015	0/0
33	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	07/2015 -	07/2015	0/0
34	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,MULTI STATE	08/2011	586.00 -	08/2015 -	08/2015	0/0
35	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	11/2012	309.81 -	10/2014 -	10/2015	0/0
36	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	12/2014 -	10/2015	0/0
37	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,MAHARASHTRA	01/2007	2,323.40 2,920.82	09/2010 03/2012	12/2015	0/0
38	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18 -	01/2013 -	12/2015	0/0
39	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	12/2012	607.06 -	01/2016 -	12/2015	0/0
40	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]ONGC,MAHARASHTRA	12/2012	3,513.07 -	02/2016 -	02/2016	0/0
41	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE	05/2013	4,124.35 -	04/2016 -	04/2016	0/0
42	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL,KERALA	01/1999	14,225.00 -	12/2015 -	05/2016	0/0

			(March 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
43	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,MULTI STATE	04/2003	429.82 2,735.65	04/2006 06/2012	06/2016	0/0
44	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	03/2013 -	06/2016	0/0
45	AHMEDABAD REDEVELOPMENT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10 -	12/2014 -	12/2016	0/0
46	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63 -	12/2014 -	12/2016	0/0
47	MEHESANA REDEVELOPMENT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	04/2015 -	03/2017	0/0
48	CREATION OF SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND ETP AT MADHUBAN - [N16000167]OIL,MULTI STATE	08/2006	374.56 -	09/2012 -	03/2017	0/0
49	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	- -	-	0/0
	Total		91,747.10 -			0/0
	<u>POWER</u>					
50	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]PGCIL,ANDHRA PRADESH	02/2014	243.53 -	08/2014 -	08/2014	0/0
51	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	09/2014 -	09/2014	0/0
52	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	06/2015 -	06/2015	0/0
53	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]PGCIL,ANDHRA PRADESH	06/2012	1,909.24 -	06/2015 -	06/2015	0/0
54	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]PGCIL,KARNATAKA	02/2014	167.40 -	12/2015 -	12/2015	0/0
55	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL,MULTI STATE	09/2013	680.69 -	03/2016 -	03/2016	0/0
56	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	04/2016 -	04/2016	0/0
57	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL,MULTI STATE	09/2013	1,575.30 -	05/2016 -	05/2016	0/0
58	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	05/2016 -	05/2016	0/0
59	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 -	06/2016 -	06/2016	0/0
60	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL,MULTI STATE	02/2014	908.08 -	06/2016 -	06/2016	0/0
61	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154]PGCIL,MAHARASHTRA	10/2013	1,315.90 -	11/2016 -	11/2016	0/0
62	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	07/2018	0/0
	Total		16,077.27 -			0/0
	<u>RAILWAYS</u>					

			(March 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
63	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	409.00 625.30	06/2007 -	06/2007	0/0
64	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,ANDHRA PRADESH	07/1998	125.00 -	07/2008 -	07/2008	0/0
65	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	- 05/2009	05/2009	0/0
66	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	371.36 768.87	- 03/2010	03/2010	0/0
67	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	907.69 3,156.32	12/2006 08/2010	08/2010	0/0
68	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	225.68 293.74	12/2010 12/2010	12/2010	0/0
69	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	120.90 663.01	06/1999 03/2011	03/2011	0/0
70	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,MULTI STATE	12/2006	170.00 170.00	03/2011 03/2011	03/2011	0/0
71	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011	0/0
72	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	02/2012	0/0
73	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	157.96 1,188.91	- 12/2009	02/2012	0/0
74	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	259.51 533.38	12/2011 02/2012	02/2012	0/0
75	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 429.49	02/2009 -	03/2012	0/0
76	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,UTTAR PRADESH	03/2002	381.17 863.23	- -	03/2012	0/0
77	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N22000052]WS&PU,BIHAR	04/2003	98.74 224.51	- -	03/2012	0/0
78	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,BIHAR	03/2005	470.09 1,417.97	- -	03/2012	0/0
79	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 155.00	- -	10/2012	0/0
80	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	190.81 238.56	03/2012 03/2012	12/2012	0/0
81	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 343.17	- -	12/2012	0/0
82	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 412.91	- -	01/2013	0/0
83	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	138.00 607.09	12/2012 12/2012	02/2013	0/0
84	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 218.19	- -	02/2013	0/0
85	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	02/2013	0/0
86	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	184.00 900.05	12/2011 12/2011	03/2013	0/0
87	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,UTTAR PRADESH	03/1997	395.00 1,577.45	- -	03/2013	0/0

			(March 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
88	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	02/2011 02/2011	03/2013	0/0
89	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	323.41 322.95	03/2012 03/2013	03/2013	0/0
90	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	114.01 332.92	03/2012 03/2013	03/2013	0/0
91	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	03/2013 -	03/2013	0/0
92	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	189.97 -	12/2011 11/2013	11/2013	0/0
93	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- -	12/2013	0/0
94	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	03/1994 -	01/2014	0/0
95	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,ANDHRA PRADESH	12/1994	124.43 495.68	- -	02/2014	0/0
96	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	151.84 410.08	- -	03/2014	0/0
97	MUNEERABAD-MAHABOONAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 377.32	- -	03/2014	0/0
98	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	12/2009 03/2011	03/2014	0/0
99	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 230.03	- -	03/2014	0/0
100	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR - [N22000083]NEFR,ARUNACHAL PRADESH	09/1996	156.00 156.00	- -	03/2014	0/0
101	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 224.89	03/2012 12/2013	03/2014	0/0
102	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII-MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 482.70	03/2013 -	03/2014	0/0
103	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 653.19	03/2014 -	03/2014	0/0
104	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 516.23	03/2014 -	03/2014	0/0
105	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	03/2014 -	03/2014	0/0
106	NEW BG LINE FROM DUDHNOI-MENDIPATAR - [N22000192]NEFR,MULTI STATE	04/1999	175.43 -	- -	03/2014	0/0
107	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2014	0/0
108	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	203.00 -	- -	03/2014	0/0
109	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	- -	04/2014	0/0
110	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	191.00 -	- -	05/2014	0/0
111	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	146.95 -	06/2013 -	06/2014	0/0
112	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	02/2009 02/2009	08/2014	0/0

			(March 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
113	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	03/2009 03/2009	08/2014	0/0
114	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	09/2001	120.00 245.39	12/2008 -	09/2014	0/0
115	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	401.81 495.44	03/2004 12/2010	12/2014	0/0
116	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 194.07	06/2004 -	12/2014	0/0
117	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	355.38 470.21	- -	12/2014	0/0
118	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 2,363.00	03/2009 12/2012	12/2014	0/0
119	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 207.52	12/2012 -	12/2014	0/0
120	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00 -	- -	12/2014	0/0
121	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	02/2015 -	02/2015	0/0
122	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,MULTI STATE	03/1984	520.00 835.04	03/1995 -	03/2015	0/0
123	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NEFR,WEST BENGAL	04/1983	36.80 274.41	- -	03/2015	0/0
124	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]RE,WEST BENGAL	04/1974	31.42 393.46	03/2007 03/2007	03/2015	0/0
125	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,BIHAR	09/2001	100.00 492.98	12/2010 12/2010	03/2015	0/0
126	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]NEFR,MULTI STATE	01/2004	915.70 915.70	- -	03/2015	0/0
127	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	06/2013 06/2013	03/2015	0/0
128	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,BIHAR	04/2008	282.92 282.92	- -	03/2015	0/0
129	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 829.74	03/2015 -	03/2015	0/0
130	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 -	03/2015 -	03/2015	0/0
131	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	186.92 261.70	02/2006 -	06/2015	0/0
132	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 2,921.00	10/2007 12/2012	12/2015	0/0
133	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	03/2010 -	12/2015	0/0
134	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	12/2015	0/0
135	DANGOAPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	12/2015 -	12/2015	0/0
136	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	03/2016	0/0
137	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	03/2016 -	03/2016	0/0

			(March 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
138	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,619.02 -	03/2016 -	03/2016	0/0
139	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	03/2016	0/0
140	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER, JHARKHAND	04/2012	258.20 -	- -	03/2016	0/0
141	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NEFR, MULTI STATE	04/2010	241.52 -	- -	03/2016	0/0
142	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NEFR, ASSAM	04/2011	312.12 -	- -	03/2016	0/0
143	HYDERABAD/SECUNDERABD MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II - [N22000213]MRTP, ANDHRA PRADESH	04/2012	632.68 -	04/2012 -	03/2016	0/0
144	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97 1,013.74	06/2005 07/2011	06/2016	0/0
145	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	06/2016	0/0
146	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	03/2005 12/2008	12/2016	0/0
147	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 5,300.00	03/2014 03/2016	12/2016	0/0
148	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR, MANIPUR	04/2003	727.56 727.53	03/2011 03/2014	03/2017	0/0
149	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR, UTTAR PRADESH	04/2006	325.00 325.00	03/2010 03/2017	03/2017	0/0
150	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR, TRIPURA	04/2008	813.34 813.34	03/2014 -	03/2017	0/0
151	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR, MIZORAM	04/2008	619.34 -	04/2014 -	03/2017	0/0
152	SEVOK RANGPO, NEFR - [N22000102]NEFR, SIKKIM	04/2008	1,339.48 -	12/2015 -	03/2017	0/0
153	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NEFR, NAGALAND	04/2006	850.00 850.00	03/2015 -	03/2017	0/0
154	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NEFR, ASSAM	04/1996	1,676.31 1,676.31	03/2009 -	03/2017	0/0
155	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NEFR, TRIPURA	04/1999	895.00 -	03/2007 -	03/2017	0/0
156	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NEFR, WEST BENGAL	04/2011	209.77 -	- -	03/2017	0/0
157	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NEFR, WEST BENGAL	04/2012	283.55 -	- -	03/2017	0/0
158	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER, MULTI STATE	04/2011	299.60 -	03/2017 -	03/2017	0/0
159	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER, MULTI STATE	04/2010	423.66 -	03/2017 -	03/2017	0/0
160	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, JAMMU AND KASHMIR	03/1995	2,500.00 2,500.00	11/2002 -	12/2017	0/0
161	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES, NEFR - [220100201]NEFR, ASSAM	09/1997	1,000.00 1,500.00	04/2008 03/2014	12/2017	0/0
162	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	- 12/2017	12/2017	0/0

			(March 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
163	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NEFR, MULTI STATE	04/2000	733.00 733.00	12/2008 -	03/2018	0/0
164	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NEFR, ASSAM	09/2006	200.00 200.00	- -	03/2018	0/0
165	KATAKHAL TO BHAIRABI - [N22000126]NEFR, ASSAM	04/1998	227.90 227.90	12/2012 -	03/2018	0/0
166	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]NCR, MULTI STATE	04/2010	622.41 2,030.50	02/2019 -	02/2019	0/0
167	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR, MULTI STATE	04/2011	1,176.09 3,845.60	02/2020 -	02/2020	0/0
168	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL - [220100149]RVNL, CHHATISGARH	04/1995	304.00 -	12/2012 -	-	0/0
169	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, MULTI STATE	02/1997	386.30 1,038.00	03/1998 -	-	0/0
170	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR, KERALA	10/1998	550.00 517.70	- -	-	0/0
171	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, ODISHA	04/1996	301.64 -	- 09/2009	-	0/0
172	KODERMA-TILAIYA (NL), ECR - [220100305]ECR, JHARKHAND	04/2002	459.91 418.17	- -	-	0/0
173	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL, ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-	0/0
174	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-	0/0
175	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL, CHHATISGARH	09/2006	324.90 -	03/2010 -	-	0/0
176	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER, UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0
177	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER, MULTI STATE	03/2007	243.78 -	- -	-	0/0
178	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER, UTTAR PRADESH	03/2008	195.64 -	- -	-	0/0
179	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER, UTTAR PRADESH	03/2012	160.89 199.75	- -	-	0/0
180	CHHAPRA-BALLIA UP - [N22000134]NER, MULTI STATE	03/2013	295.00 295.00	- -	-	0/0
181	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER, UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
182	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR, RAJASTHAN	04/2012	246.08 -	- -	-	0/0
183	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR, MULTI STATE	04/2007	1,347.26 -	- -	-	0/0
184	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR, MULTI STATE	04/2007	1,640.04 -	- -	-	0/0
185	AHMEDABAD-BOTAD (GC) - [N22000140]WR, GUJARAT	04/2012	567.18 -	- -	-	0/0
186	DHASA-JETALSAR (GC) - [N22000141]WR, GUJARAT	04/2012	376.59 -	- -	-	0/0
187	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR, GUJARAT	04/2011	439.88 -	- -	-	0/0

			(March 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
188	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 -	- -	-	0/0
189	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT	04/2013	1,266.89 -	- -	-	0/0
190	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	- -	-	0/0
191	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2012	2,082.75 -	- -	-	0/0
192	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	-	0/0
193	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-	0/0
194	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0
195	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	- -	-	0/0
196	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	- -	-	0/0
197	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	- -	-	0/0
198	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	- -	-	0/0
199	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	- -	-	0/0
200	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	- -	-	0/0
201	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- -	-	0/0
202	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SWR,MULTI STATE	04/2010	553.63 -	- -	-	0/0
203	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	- -	-	0/0
204	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	- -	-	0/0
205	NAWADA-LAXMIPUR (NL) - [N22000167]SER,BIHAR	04/2008	620.57 -	- -	-	0/0
206	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-	0/0
207	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-	0/0
208	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-	0/0
209	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-	0/0
210	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-	0/0
211	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	366.73 -	- -	-	0/0
212	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-	0/0

			(March 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
213	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-	0/0
214	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-	0/0
215	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-	0/0
216	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-	0/0
217	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-	0/0
218	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-	0/0
219	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-	0/0
220	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-	0/0
221	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NEFR,MULTI STATE	04/2013	1,798.00 -	- -	-	0/0
222	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	- -	-	0/0
223	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-	0/0
224	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-	0/0
225	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-	0/0
226	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1999	271.24 -	- -	-	0/0
227	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	- -	-	0/0
228	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-	0/0
229	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-	0/0
230	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NEFR,WEST BENGAL	04/2010	221.42 -	- -	-	0/0
231	AGARTALA-AKHAURA NL - [N22000195]NEFR,TRIPURA	04/2012	252.00 -	- -	-	0/0
232	DIMAPUR-TIZIT NL - [N22000196]NEFR,NAGALAND	04/2013	4,274.00 -	- -	-	0/0
233	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-	0/0
234	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-	0/0
235	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-	0/0
236	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-	0/0
237	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NEFR,MEGHALAYA	04/2010	4,083.02 -	- -	-	0/0

			(March 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
238	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NEFR,MULTI STATE	04/2010	242.22 -	- -	-	0/0
239	MURKONGSELEK-PASIGHAT NL - [N22000208]NEFR,MULTI STATE	04/2011	165.82 -	- -	-	0/0
240	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NEFR,MULTI STATE	04/1999	523.17 -	- -	-	0/0
241	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NEFR,ASSAM	04/2012	246.07 -	- -	-	0/0
242	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-	0/0
243	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-	0/0
244	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1999	406.99 -	- -	-	0/0
245	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-	0/0
246	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-	0/0
247	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-	0/0
248	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-	0/0
249	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-	0/0
250	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-	0/0
251	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-	0/0
252	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-	0/0
253	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-	0/0
254	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-	0/0
255	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-	0/0
256	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-	0/0
257	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	697.00 -	- -	-	0/0
258	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-	0/0
259	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-	0/0
260	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-	0/0
261	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-	0/0

			(March 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
262	SAINTIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-	0/0
263	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-	0/0
264	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-	0/0
265	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-	0/0
266	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-	0/0
267	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-	0/0
268	NABADWIPDHAM-PATULI DOUBLING - [N22000246]ER,MULTI STATE	04/2010	169.82 -	- -	-	0/0
269	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	182.06 -	- -	-	0/0
270	SANTOSHPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-	0/0
271	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-	0/0
272	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-	0/0
273	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-	0/0
274	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-	0/0
275	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	- -	-	0/0
276	MANUGURU-RAMAGUNDAM - [N22000259](SCR),ANDHRA PRADESH	04/2013	1,112.00 -	- -	-	0/0
277	KONDAPALLI-PENUBALLI - [N22000260](SCR),ANDHRA PRADESH	04/2013	723.00 -	- -	-	0/0
278	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261](SCR),MULTI STATE	04/2012	1,054.35 -	- -	-	0/0
279	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263](SCR),MULTI STATE	04/2008	184.26 -	- -	-	0/0
280	BHADRACHALAM-KOVVUR - [N22000264](SCR),ANDHRA PRADESH	04/2012	923.23 -	- -	-	0/0
281	GUDUR-DURGARAJAPATNAM - [N22000265](SCR),ANDHRA PRADESH	04/2011	283.54 -	- -	-	0/0
282	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	289.79 -	- -	-	0/0
283	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	159.20 -	- -	-	0/0
284	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-	0/0
285	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-	0/0
286	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-	0/0

			(March 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
287	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-	0/0
288	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	-	0/0
289	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-	0/0
290	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-	0/0
291	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	- -	-	0/0
292	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-	0/0
293	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-	0/0
294	CUMBUM-PRODDATUR - [N22000282](SCR),ANDHRA PRADESH	04/2013	829.00 -	- -	-	0/0
295	MUDKHED-PARBHANI - [N22000283](SCR),MAHARASHTRA	04/2011	390.60 -	- -	-	0/0
296	AKKANAPET-MEDAK - [N22000285](SCR),ANDHRA PRADESH	04/2012	153.00 -	- -	-	0/0
297	NADIKUDE-SRI KALAHASTI - [N22000286](SCR),ANDHRA PRADESH	04/2011	1,313.48 -	- -	-	0/0
298	BHADRACHALAM ROAD-SATTUPALLI - [N22000287](SCR),ANDHRA PRADESH	04/2010	337.49 -	- -	-	0/0
299	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288](SCR),MULTI STATE	04/2008	2,050.00 -	- -	-	0/0
300	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-	0/0
301	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	165.65 -	- -	-	0/0
302	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-	0/0
303	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-	0/0
304	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-	0/0
305	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-	0/0
306	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-	0/0
307	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	- -	-	0/0
308	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	- -	-	0/0
309	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	-	0/0
310	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-	0/0
311	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	01/1999 -	-	0/0

			(March 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
312	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,ANDHRA PRADESH	04/2007	313.24 -	01/1999 -	-	0/0
313	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-	0/0
314	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	01/1999 -	-	0/0
315	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-	0/0
316	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 -	- 03/2010	-	0/0
317	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	353.08 514.68	- -	-	0/0
318	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	37.68 450.00	07/2012 -	-	0/0
319	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	- -	-	0/0
320	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	491.19 2,957.21	07/2005 -	-	0/0
321	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,MULTI STATE	09/1998	925.00 -	05/2008 03/2011	-	0/0
322	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	233.00 501.69	03/2012 08/2012	-	0/0
323	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	78.23 162.87	- -	-	0/0
324	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 100.00	- -	-	0/0
325	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 1,047.00	- -	-	0/0
326	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	02/1999	138.00 901.62	- -	-	0/0
327	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	324.66 528.65	- -	-	0/0
328	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	104.79 -	- -	-	0/0
329	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	727.13 727.13	- -	-	0/0
330	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	726.96 810.78	- -	-	0/0
331	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,ANDHRA PRADESH	04/2006	378.56 671.82	- -	-	0/0
332	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 404.19	- -	-	0/0
333	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 125.00	- -	-	0/0
334	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 456.00	- -	-	0/0
335	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NEFR,BIHAR	09/2006	300.00 300.00	- -	-	0/0
336	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-	0/0

			(March 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
337	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	-	0/0
338	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-	0/0
339	MANSABHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-	0/0
340	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-	0/0
341	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-	0/0
342	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-	0/0
	Total		147,948.15 -			0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
343	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,ANDHRA PRADESH	02/2010	390.56 -	02/2012 -	06/2013	0/0
344	2 LANING OF MUZAFFARPUR - SONBARSA - [N24000174]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	11/2013	0/0
345	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 157.47	09/2007 03/2014	12/2013	0/0
346	SIX LANNING OF HOSUR- KRISHNAGIRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	12/2013 -	12/2013	0/0
347	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	12/2013	0/0
348	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	01/2014	0/0
349	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	01/2014 -	01/2014	0/0
350	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	01/2014 -	01/2014	0/0
351	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	01/2014 -	01/2014	0/0
352	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	01/2014	0/0
353	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	02/2014 -	02/2014	0/0
354	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	02/2014 -	02/2014	0/0
355	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	02/2014 -	02/2014	0/0
356	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	03/2014	0/0
357	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014 -	03/2014	0/0
358	PATNA-BAKTARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	03/2014	0/0

			(March 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
359	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	10/2013 -	03/2014	0/0
360	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	10/2013 -	03/2014	0/0
361	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 331.23	07/2009 -	04/2014	0/0
362	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	04/2014	0/0
363	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	04/2014 -	04/2014	0/0
364	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 361.00	02/2009 -	05/2014	0/0
365	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 05/2014	05/2014	0/0
366	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 333.83	09/2007 -	05/2014	0/0
367	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	05/2014	0/0
368	2LANING WITH PS GOPALGANJ-CHAPRA - [N24000190]NHAI,BIHAR	12/2011	325.00 -	05/2014 -	05/2014	0/0
369	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	05/2014 -	05/2014	0/0
370	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 1,141.00	08/2013 06/2014	06/2014	0/0
371	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	06/2014 -	06/2014	0/0
372	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	06/2014 -	06/2014	0/0
373	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	06/2014 -	06/2014	0/0
374	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 07/2014	07/2014	0/0
375	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	09/2013 -	07/2014	0/0
376	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	07/2014 -	07/2014	0/0
377	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	07/2014 -	07/2014	0/0
378	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	07/2014 -	07/2014	0/0
379	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	08/2014	0/0
380	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	09/2014	0/0
381	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	09/2014	0/0
382	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN	03/2012	333.51 -	09/2014 -	09/2014	0/0
383	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00 -	10/2014 -	10/2014	0/0

			(March 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
384	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19 -	10/2014 -	10/2014	0/0
385	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH	10/2012	250.50 -	10/2014 -	10/2014	0/0
386	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]NHAI,MADHYA PRADESH	10/2011	1,565.00 -	10/2014 -	10/2014	0/0
387	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 382.02	04/2009 12/2014	12/2014	0/0
388	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 265.53	11/2008 12/2014	12/2014	0/0
389	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 241.28	11/2008 12/2014	12/2014	0/0
390	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 247.43	04/2009 12/2014	12/2014	0/0
391	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	04/2008 01/2015	01/2015	0/0
392	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 01/2015	01/2015	0/0
393	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	04/2008 01/2015	01/2015	0/0
394	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	04/2008 01/2015	01/2015	0/0
395	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	02/2015 -	02/2015	0/0
396	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	04/2015 -	04/2015	0/0
397	NASHRI CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	06/2010	2,159.00 -	06/2015 -	06/2015	0/0
398	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,MULTI STATE	12/2012	1,479.00 -	06/2015 -	06/2015	0/0
399	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	07/2015	0/0
400	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00 -	08/2015 -	08/2015	0/0
401	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	09/2015	0/0
402	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	11/2015 -	11/2015	0/0
403	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	04/2010 01/2016	01/2016	0/0
404	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	09/2008 -	-	0/0
405	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	06/2005 -	-	0/0
406	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,JAMMU AND KASHMIR	12/2003	166.27 -	03/2008 -	-	0/0
407	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	10/2008 -	-	0/0
408	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	06/2008 -	-	0/0

			(March 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
409	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	06/2008 -	-	0/0
410	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	09/2008 -	-	0/0
411	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	10/2008 -	-	0/0
412	RAJMARG CHORAH TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	10/2008 -	-	0/0
413	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	07/2008 -	-	0/0
414	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-	0/0
415	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	06/2008 -	-	0/0
416	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-	0/0
417	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	02/2010 -	-	0/0
418	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-	0/0
419	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 385.15	09/2007 07/2011	-	0/0
420	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	02/2010 -	-	0/0
421	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	09/2010 -	-	0/0
422	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	07/2012 -	-	0/0
423	PUNE-SHOLAPUR,PKG1 - [N24000127]NHAI,MAHARASHTRA	11/2009	1,110.00 -	05/2012 -	-	0/0
424	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	05/2012 -	-	0/0
425	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	10/2011 -	-	0/0
426	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	10/2011 -	-	0/0
427	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	-	0/0
428	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	12/2012 -	-	0/0
429	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	-	0/0
430	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	09/2013 -	-	0/0
431	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	-	0/0
432	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	01/2013 -	-	0/0
433	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	03/2013 -	-	0/0

			(March 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
434	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	-	0/0
435	AMRITSAR-PATHANKOT - [N24000147]NHAI,PUNJAB	05/2010	705.00 -	11/2012 -	-	0/0
436	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	07/2013 -	-	0/0
437	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	-	0/0
438	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	11/2012 -	-	0/0
439	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	06/2013 -	-	0/0
440	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	-	0/0
441	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-	0/0
442	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-	0/0
443	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	-	0/0
444	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	-	0/0
445	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	-	0/0
446	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	-	0/0
447	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	-	0/0
448	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	-	0/0
449	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,TAMIL NADU	04/2011	571.00 -	10/2013 -	-	0/0
450	SAMAKHIALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	03/2013 -	-	0/0
451	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	-	0/0
452	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	-	0/0
453	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	-	0/0
454	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	01/2013 -	-	0/0
455	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	08/2013 -	-	0/0
456	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	02/2013 -	-	0/0
457	BAREILY-SITAPUR - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	-	0/0
458	MUZZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	-	0/0

			(March 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
459	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	08/2013 -	-	0/0
460	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	08/2013 -	-	0/0
461	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	08/2013 -	-	0/0
462	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	07/2012 -	-	0/0
463	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	- -	-	0/0
	Total		86,111.81 -			0/0
	<u>SHIPPING AND PORTS</u>					
464	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 298.17	04/2009 11/2009	02/2011	0/0
465	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY VESSELS - [N25000014]SHIPP.,MAHARASHTRA	10/2007	359.44 -	04/2011 11/2011	11/2011	0/0
466	MODIFICATION & STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST,GUJARAT	06/2010	277.00 -	03/2012 -	03/2012	0/0
467	ACQUISITION OF TWO NOS. OF 3060 DWT - [N25000043]SHIPP.,MAHARASHTRA	04/2009	277.03 280.00	12/2011 10/2012	10/2012	0/0
468	MECHANIZATION OF COAL HANDLING FACILITIES TO 200000 DWT VESSELS ON DBFOT BASIS - [N25000049]PORT TRUST,ANDHRA PRADESH	02/2010	444.10 -	06/2010 -	11/2012	0/0
469	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST - [N25000037]PORT TRUST,GUJARAT	04/2005	882.00 -	02/2011 -	12/2012	0/0
470	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,GUJARAT	12/2005	702.00 -	03/2011 -	03/2013	0/0
471	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST,GUJARAT	02/2011	830.00 -	05/2013 -	05/2013	0/0
472	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,MULTI STATE	07/2011	220.49 -	01/2013 06/2013	06/2013	0/0
473	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN - [N25000048]PORT TRUST,KERALA	03/2009	3,500.00 4,150.00	01/2012 09/2012	08/2013	0/0
474	ACQUISITION OF 4 NOS OF 82000 DWT KAMSAVMAX BULK CARRIERS FROM M/S JIANGSU EASTERN HEAVY INDUSTRIES - [N25000051]SHIPP.,MAHARASHTRA	08/2010	612.72 532.83	12/2012 11/2013	11/2013	0/0
475	ACQUISITION OF THREE(3) NOS OF 6500TEU CELLULAR CONTAINER VESSELS FROM M/S STX SHIPBUILDING CO. LTD. - [N25000052]SHIPP.,MAHARASHTRA	10/2010	1,028.10 1,012.23	12/2013 11/2013	11/2013	0/0
476	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053]SHIPP.,MAHARASHTRA	10/2010	966.46 -	02/2014 04/2014	04/2014	0/0
477	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 309.00	03/2006 06/2014	06/2014	0/0
478	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY - [N25000062]SHIPP.,MULTI STATE	01/2012	511.87 -	03/2014 08/2014	08/2014	0/0
479	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 1,460.00	12/2010 09/2012	10/2015	0/0
480	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 11/2010	-	0/0

			(March 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
481	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL - [N25000003]PORT TRUST,MAHARASHTRA	10/2005	800.00 1,571.60	10/2008 -	-	0/0
	Total		15,462.28 -			0/0
	<u>TELECOMMUNICATIONS</u>					
482	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) PH-5.1 PUNJAB - [N26000041]BSNL,PUNJAB	02/2008	373.94 -	12/2008 -	12/2012	0/0
483	GSM EQUIPMENT OF 799000LINES (2G) 101000 LINES 3(G) JHARKHANDPHASE V.1 TELECOM CIRCLE - [N26000088]BSNL,JHARKHAND	03/2008	328.13 -	03/2009 -	01/2013	0/0
484	GSM EQUIPMENT OF 1625000LINES (2G) 325000 LINES 3(G) MP PHASE V.1 TELECOM CIRCLE - [N26000090]BSNL,MADHYA PRADESH	11/2009	916.70 -	11/2010 12/2012	09/2013	0/0
485	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	10/2010 03/2012	03/2014	0/0
486	SUPPLY INSTALLATION TESTING AND COMMISSIONING OF RURAL WIMAX NETWORK PHASE-II - [N26000100]BSNL,MULTI STATE	07/2010	1,148.19 -	05/2011 -	05/2014	0/0
487	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTARANCHAL - [N26000058]BSNL,UTTARAKHAND	01/2009	149.15 -	06/2009 -	06/2014	0/0
488	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL,ASSAM	06/2007	336.81 -	01/2009 -	06/2014	0/0
489	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK.PROCUREMENT OF GPON EQUIPMANT - [N26000072]BSNL,MULTI STATE	12/2007	952.88 -	03/2010 -	-	0/0
490	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK,PROCUREMENT OF GEPOE EQUIPMENT - [N26000073]BSNL,MULTI STATE	12/2007	152.65 -	03/2010 -	-	0/0
491	GSM EQUIPMENT OF 200000LINES (2G) UP(WEST)PHASE V.2 TELECOM CIRCLE - [N26000082]BSNL,UTTAR PRADESH	10/2008	336.84 -	10/2009 -	-	0/0
	Total		5,079.29 -			0/0
	<u>URBAN DEVELOPMENT</u>					
492	FARIDABAD EXTENSION - [N28000057]DMRC,DELHI	09/2011	2,494.00 -	09/2014 -	05/2015	0/0
493	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	03/2016 -	03/2016	0/0
494	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA	02/2014	26,405.14 -	02/2019 -	02/2019	0/0
495	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI - [N28000048]CPWD,MAHARASHTRA	11/2006	114.18 173.08	04/2009 -	-	0/0
	Total		67,598.32 -			0/0
	<u>WATER RESOURCES</u>					
496	PAGLADIYA DAM PROJECT - [300100001]MOWR,ASSAM	01/2001	542.90 -	12/2007 -	12/2012	0/0
	Total		542.90 -			0/0

			(March 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	Grand Total		436,840.55			0/0

List of Ongoing Projects having Time and Cost Overrun w.r.t Original Schedule

(March 2014)								
					Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	T.O.R (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	03/2015	62.57	54
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	12/2008 -	12/2014	31.12	72
	Total		16,663.00 -	22,947.00				
	<u>CIVIL AVIATION</u>							
3	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]	05/2010	335.61 -	388.53	05/2012 -	04/2014	15.77	23
	Total		335.61 -	23,335.53				
	<u>COAL</u>							
4	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	03/2015	478.50	24
5	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]	12/2009	321.42 -	321.50	03/2014 -	03/2016	0.02	24
6	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37	44
7	KUSMUNDA EXPN.OCP(SECL)(10-15)MTY - [N06000008]	06/2008	1,188.31 -	7,612.33	03/2013 -	03/2023	540.60	120
8	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,027.59	06/2009 -	06/2014	49.09	60
9	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,602.74	03/2012 -	08/2014	34.63	29
	Total		9,127.17 -	42,834.48				
	<u>PETROLEUM</u>							
10	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]	08/2008	144.02 -	204.29	06/2012 -	06/2014	41.85	24
11	CONSTRUCTION OF SIX EFFLUENT TREATMENT PLANTS (ETP), AHMEDABAD AND ANKLESWAR - [N16000099]	03/2009	234.78 234.78	317.64	09/2012 -	12/2014	35.29	27
12	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]	08/2009	246.81 -	276.83	04/2012 -	06/2014	12.16	26
13	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	11/2012	309.81 -	309.82	10/2014 -	10/2015	0.00	12
14	DEV OF G1 AND GS-15 (ONGCL) - [160100231]	04/2003	429.82 -	2,735.65	04/2006 -	06/2016	536.46	122

List of Ongoing Projects having Cost Overrun w.r.t. to Original Schedule

(March 2014)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	12/2008 -	12/2014	31.12
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	03/2015	62.57
	Total		16,663.00 -	22,947.00			
	<u>CIVIL AVIATION</u>						
3	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]	08/2008	1,942.51 -	2,593.13	05/2011 -	03/2013	33.49
4	D/O KAMARAJ DOMESTIC TER-PH-II AND EXP. ANNA INT. TER BLDG(K1) - [N04000038]	08/2008	1,808.00 -	2,015.00	01/2011 -	02/2012	11.45
5	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]	05/2010	335.61 -	388.53	05/2012 -	04/2014	15.77
	Total		4,086.12 -	27,943.66			
	<u>COAL</u>						
6	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,027.59	06/2009 -	06/2014	49.09
7	KUSMUNDA EXPN.OCP(SECL)(10-15)MTY - [N06000008]	06/2008	1,188.31 -	7,612.33	03/2013 -	03/2023	540.60
8	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37
9	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	03/2015	478.50
10	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.00 -	490.10	03/2017 -	03/2017	0.02
11	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,602.74	03/2012 -	08/2014	34.63
12	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]	12/2009	321.42 -	321.50	03/2014 -	03/2016	0.02
13	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	03/2016 -	03/2016	31.87
	Total		9,767.76 -	48,131.30			
	<u>PETROCHEMICALS</u>						
14	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	8,920.00	04/2012 -	-	63.35

(March 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	Total		5,460.61 -	57,051.30			
	<u>PETROLEUM</u>						
15	DEV OF G1 AND GS-15 (ONGCL) - [N160100231	04/2003	429.82 -	2,735.65	04/2006 -	06/2016	536.46
16	DEVELOPMENT OF C-SERIES FIELDS - [N16000023	08/2006	3,195.16 -	3,690.37	12/2008 -	09/2014	15.50
17	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032	01/2007	2,323.40 -	2,920.82	09/2010 03/2012	12/2015	25.71
18	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033	06/2007	3,248.78 -	5,633.44	08/2010 03/2012	05/2014	73.40
19	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039	10/2007	5,713.03 -	8,813.41	05/2010 -	05/2014	54.27
20	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046	06/2007	1,436.21 1,456.96	1,456.96	07/2010 05/2012	05/2014	1.44
21	PARADIP REFINERY PROJECT - [N16000058	02/2009	29,777.00 -	32,710.00	11/2012 -	12/2014	9.85
22	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I - [N16000070	07/2009	238.68 -	312.00	01/2012 -	07/2013	30.72
23	ADDITIONAL DEV. OF D-1 FIELD - [N16000086	01/2010	2,163.64 -	2,331.62	06/2012 -	05/2014	7.76
24	CONSTRUCTION OF SIX EFFLUENT TREATMENT PLANTS (ETP), AHMEDABAD AND ANKLESWAR - [N16000099	03/2009	234.78 234.78	317.64	09/2012 -	12/2014	35.29
25	WAX PROJECT - [N16000101	06/2010	576.60 -	676.05	12/2013 -	03/2014	17.25
26	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104	03/2010	3,241.03 -	6,638.94	03/2013 -	11/2014	104.84
27	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131	12/2011	2,059.63 -	2,665.65	03/2015 -	03/2015	29.42
28	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138	08/2009	246.81 -	276.83	04/2012 -	06/2014	12.16
29	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146	11/2012	666.00 -	701.00	11/2015 -	11/2015	5.26
30	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155	11/2012	309.81 -	309.82	10/2014 -	10/2015	0.00
31	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156	01/2006	672.00 -	1,038.00	10/2011 -	09/2014	54.46
32	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157	01/2006	732.00 -	1,227.00	10/2011 -	06/2015	67.62
33	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169	01/2006	993.00 -	1,693.00	01/2012 -	06/2015	70.49
34	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149	08/2008	144.02 -	204.29	06/2012 -	06/2014	41.85
	Total		58,401.40 -	133,403.79			

(March 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>POWER</u>						
35	PARBATI HEP (NHPC) II - [180100210]	09/2002	3,919.59 -	5,366.00	09/2009 -	07/2018	36.90
36	KOLDAM HEP (NTPC) - [180100211]	10/2002	4,527.15 -	7,220.00	04/2009 -	05/2015	59.48
37	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]	09/2003	6,285.33 -	10,667.00	09/2010 -	07/2018	69.71
38	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	4,653.95	12/2009 06/2016	03/2017	86.39
39	BARH STPP(3X660MW) NTPC - [180100242]	12/2003	8,692.97 -	8,693.00	12/2009 -	03/2017	0.00
40	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]	09/2005	1,061.38 -	1,501.75	09/2009 -	07/2015	41.49
41	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]	03/2005	596.45 -	1,007.16	12/2007 -	-	68.86
42	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]	10/2005	2,304.56 -	2,716.00	10/2010 -	08/2014	17.85
43	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,159.07	09/2008 -	03/2013	21.34
44	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	07/2010 -	02/2017	79.77
45	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	03/2017	29.14
46	KISHANGANGA HEP - [N18000031]	07/2007	2,238.67 -	3,642.00	01/2016 -	11/2016	62.69
47	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,745.08	07/2014 -	07/2018	50.31
48	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,128.38	08/2013 -	09/2015	96.59
49	MOUDA STPP - [N18000048]	11/2008	5,459.28 -	6,010.89	08/2012 -	03/2013	10.10
50	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC [N18000065]	08/2008	2,360.95 -	2,580.90	08/2012 -	03/2014	9.32
51	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	951.48	07/2013 -	11/2014	126.00
	Total		49,844.58 -	202,271.61			
	<u>RAILWAYS</u>						
52	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]	04/1986	158.77 274.56	608.02	03/1994 -	01/2014	282.96
53	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]	03/1984	520.00 422.79	835.04	03/1995 -	03/2015	60.58
54	VIRAMGAM-BHILDI(WR),GC - [220100062]	04/1990	155.66 -	548.01	- 03/2010	-	252.06

(March 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
55	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	925.30	- -	02/2014	643.63
56	AMRAVATI-NARKHER NL(CR) - [220100118	06/1994	120.90 175.30	725.00	06/1999 -	03/2011	499.67
57	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	20,000.00	11/2002 -	12/2017	700.00
58	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135	04/1983	36.80 274.41	703.17	- -	03/2015	1,810.79
59	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	968.60	12/2012 -	-	218.62
60	CALICUT-MANGALORE (DL) (SR) - [220100151	02/1996	240.00 -	579.37	- -	02/2012	141.40
61	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	401.81 -	1,814.10	03/2004 -	12/2014	351.48
62	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168	04/1995	184.00 -	900.05	12/2011 12/2010	03/2013	389.16
63	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181	02/1997	353.08 -	2,820.00	- -	-	698.69
64	HASSAN-BANGALORE VIA SHRAVANA- BELGOLA(NL),SWR - [220100183	02/1997	295.00 -	412.91	- -	01/2013	39.97
65	DAUSA-GANGAPUR CITY(NL),NWR - [220100184	02/1997	151.84 -	410.08	- -	03/2014	170.07
66	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,038.00	03/1998 -	-	168.70
67	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	37.68 -	1,036.78	07/2012 -	-	2,651.54
68	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	800.00	- -	10/2012	414.30
69	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192	03/1996	155.74 164.36	883.00	02/2009 -	03/2012	466.97
70	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	- -	-	840.53
71	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197	03/1997	395.00 598.98	1,708.41	- -	03/2013	332.51
72	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201	09/1997	1,000.00 -	4,500.00	04/2008 12/2011	12/2017	350.00
73	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	645.00	- -	03/2014	195.55
74	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	31.42 154.30	445.40	03/2007 03/2007	03/2015	1,317.57
75	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	596.36	06/2004 -	12/2014	207.29
76	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
77	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222	03/1999	491.19 -	2,957.21	07/2005 -	-	502.05

(March 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
78	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	925.00 -	1,630.97	05/2008 -	-	76.32
79	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240	04/1997	233.00 335.77	1,043.56	03/2012 -	-	347.88
80	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	12/2009 -	03/2014	300.67
81	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	100.00 -	725.53	12/2010 -	03/2015	625.53
82	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	550.00 -	1,566.00	- -	-	184.73
83	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	832.00	- 05/2009	05/2009	243.21
84	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR- NAUTANWA GC (NER) [220100255	03/2002	381.17 -	863.23	- -	03/2012	126.47
85	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256	04/1999	323.40 -	744.71	- -	03/2014	130.28
86	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257	04/1997	78.23 -	162.87	- -	-	108.19
87	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	409.00 408.76	847.75	06/2007 -	06/2007	107.27
88	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	900.00	- -	-	800.00
89	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) - [220100263	03/1998	280.00 -	1,122.00	- -	03/2013	300.71
90	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	330.00 -	1,045.20	- -	-	216.73
91	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	1,655.81	12/2008 -	03/2018	125.90
92	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM- NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	907.69 -	3,176.10	12/2006 -	08/2010	249.91
93	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	02/2011 -	03/2013	191.48
94	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	157.96 -	1,188.91	- 12/2009	02/2012	652.67
95	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	138.00 240.59	607.09	12/2012 12/2012	02/2013	339.92
96	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	02/1999	138.00 -	901.62	- -	-	553.35
97	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	1,423.98	03/2005 12/2008	12/2016	1,172.55
98	JIND-SONEPAT (NL),NR - [220100280	01/2004	190.81 -	740.00	03/2012 -	12/2012	287.82
99	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	355.38 -	1,995.25	- -	12/2014	461.44

(March 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
100	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06
101	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	288.00	02/2009 02/2009	08/2014	73.33
102	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	4,478.17	03/2011 -	03/2017	515.51
103	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303	04/2003	324.66 -	528.65	- -	-	62.83
104	KOSI BRIDGE (NL), ECR - [220100304	04/2002	323.41 -	341.41	03/2012 -	03/2013	5.57
105	KODERMA GIRIDH (NL), ECR - [220100306	04/1996	371.36 -	768.87	- -	03/2010	107.04
106	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	03/2009 -	12/2014	156.57
107	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76
108	DANIAWAN-BIHARSARIF (NL), ECR - [220100311	04/2001	104.79 -	406.92	- -	-	288.32
109	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314	04/2001	727.13 727.13	1,225.90	- -	-	68.59
110	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315	01/2004	915.70 -	2,232.50	- -	03/2015	143.80
111	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316	04/2003	218.19 -	472.00	- -	02/2013	116.33
112	ETAWAH-MAINPURI (NL),NCR - [220100318	09/2001	120.00 -	245.39	12/2008 -	09/2014	104.49
113	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	585.93	- -	12/2013	52.67
114	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	818.29	02/2015 -	02/2015	346.59
115	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	276.00	03/2009 03/2009	08/2014	106.88
116	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	726.96 -	810.78	- -	-	11.53
117	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329	04/2003	136.62 -	289.93	12/2007 03/2010	-	112.22
118	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	114.01 283.95	477.88	03/2012 -	03/2013	319.16
119	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N220000032	04/2006	378.56 -	791.59	- -	-	109.11
120	GOELKERA-MANOHARPUR,(LD)(SER) - [N220000045	03/1997	186.92 -	261.70	02/2006 -	06/2015	40.01
121	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N220000049	07/2006	743.00 -	1,117.11	03/2008 06/2008	-	50.35
122	HARNOUT - SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N220000052	04/2003	98.74 -	337.30	- -	03/2012	241.60
123	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N220000053	03/2005	470.09 -	1,417.97	- -	03/2012	201.64

(March 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
124	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	385.54	03/2010 -	-	18.66
125	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41
126	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY'-AGASTIYAMPALLI [N22000079]	09/2007	404.19 -	1,383.45	- -	-	242.28
127	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	914.98	- -	12/2012	166.63
128	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	485.00	03/2011 -	03/2011	185.29
129	CONSTRUCTION OF NEW LINE FROM HARMATI- ITANAGAR/NARHARIAGUN, NEFR [N22000083]	09/1996	156.00 -	406.40	- -	03/2014	160.51
130	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 -	420.00	- -	-	236.00
131	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	820.00	- -	-	79.82
132	NEW B.G. LINE FROM TETELIA TO BYRNIAHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	385.20	- -	03/2018	92.60
133	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	300.00 -	532.87	- -	-	77.62
134	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,116.53	03/2010 -	03/2017	243.55
135	BARDHAMAN-KATWA (GC) - [N22000091]	04/2007	245.15 -	1,106.62	12/2010 -	03/2011	351.41
136	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	6,213.84	03/2014 -	12/2016	17.24
137	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	246.44	03/2012 -	03/2014	44.03
138	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,074.45	06/2005 -	06/2016	265.50
139	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	1,141.75	03/2014 -	03/2017	40.38
140	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,393.48	04/2014 -	03/2017	286.46
141	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	359.86	- -	03/2015	27.20
142	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	3,380.58	12/2015 -	03/2017	152.38
143	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESHI- MUSORE (SWR) - [N22000107]	04/2007	482.00 -	482.70	03/2013 -	03/2014	0.15
144	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	04/2010	2,619.02 -	2,913.51	03/2016 -	03/2016	11.24
145	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	653.47	03/2014 -	03/2014	0.04

(March 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
146	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]	04/2009	259.51 -	533.38	12/2011 -	02/2012	105.53
147	GHUTIASHARIF-CANNING (ER) - [N22000117]	04/2009	189.97 -	611.03	12/2011 -	11/2013	221.65
148	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]	04/2004	225.68 -	293.74	12/2010 -	12/2010	30.16
149	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012 -	-	135.68
150	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	484.61	03/2012 -	-	52.28
151	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]	04/2006	117.36 196.95	196.95	03/2011 -	-	67.82
152	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	4,184.84	03/2009 -	03/2017	149.65
153	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]	03/2012	160.89 -	199.75	- -	-	24.15
154	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	494.92	- -	-	67.77
155	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	913.48	- -	-	184.87
156	VIRANGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	685.17	- -	-	53.63
157	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	02/2020	226.98
158	MAYLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]	04/2013	456.00 -	965.16	- -	-	111.66
159	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	-	17.92
160	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	218.39	- -	-	2.34
161	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	02/2019	226.23
162	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	651.17	- -	-	17.62
163	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	177.38	03/2015 -	12/2015	18.33
164	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]	04/2010	146.95 -	171.02	06/2013 -	06/2014	16.38
165	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	388.67	12/2015 -	12/2015	25.60
166	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
167	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80

(March 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
168	ATTIPPATTU-PUTTUR - [N22000184]	04/2008	446.87 -	528.00	- -	-	18.16
169	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,200.00	- -	-	129.22
170	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17
171	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC [N22000188]	04/1999	271.24 -	520.00	- -	-	91.71
172	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,280.83	- -	-	55.74
173	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
174	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	222.21	- -	-	0.36
175	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,091.98	03/2007 -	03/2017	22.01
176	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22	- -	-	109.04
177	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	-	173.71
178	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	247.00 -	951.24	- -	12/2014	285.12
179	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	222.95	- -	-	16.29
180	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]	04/1999	523.17 -	1,327.78	- -	-	153.80
181	HYDERABAD/SECUNDERABD MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II - [N22000213]	04/2012	632.68 -	816.55	04/2012 -	03/2016	29.06
182	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215]	04/2011	601.43 -	800.00	- -	-	33.02
183	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	697.00 -	2,501.05	- -	-	258.83
184	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70 -	279.70	- -	-	0.72
185	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	182.06 -	184.06	- -	-	1.10
186	PANVEL PEN DOUBLING - [N22000255]	04/2006	191.00 -	260.16	- -	05/2014	36.21
187	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26
188	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	-	651.97
189	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97

(March 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
190	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]	04/2008	184.26 -	2,000.00	- -	-	985.42
191	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]	04/2012	289.79 -	377.44	- -	-	30.25
192	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	755.54	- -	-	163.25
193	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99	- -	-	183.41
194	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29
195	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	329.97	- -	-	50.10
196	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]	04/1999	460.94 -	1,030.00	01/1999 -	-	123.46
	Total		62,948.65 -	374,012.64			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
197	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00 -	201.66	09/2008 -	-	30.10
198	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236]	12/2003	166.27 -	193.10	03/2008 -	-	16.14
199	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	05/2014	28.93
200	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	382.02	04/2009 -	12/2014	91.19
201	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]	12/2003	167.64 -	265.63	11/2008 -	12/2014	58.45
202	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	241.28	11/2008 -	12/2014	55.62
203	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]	12/2003	200.00 -	247.43	04/2009 -	12/2014	23.72
204	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061]	12/2003	212.00 -	333.83	09/2007 -	05/2014	57.47
205	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	04/2014	68.99
206	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	04/2010 -	01/2016	42.25
207	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	-	2.29
208	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]	12/2003	348.16 -	385.15	09/2007 -	-	10.62
209	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	-	106.50
	Total		3,680.53 -	379,833.84			

(March 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>SHIPPING AND PORTS</u>						
210	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL - [N25000003]	10/2005	800.00 -	1,571.60	10/2008 -	-	96.45
211	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]	12/2005	154.84 -	253.36	- 01/2009	12/2010	63.63
212	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]	11/2007	1,228.00 -	2,158.16	12/2010 -	10/2015	75.75
213	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	03/2006 -	06/2014	300.00
214	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST - [N25000037]	04/2005	882.00 -	1,060.00	02/2011 -	12/2012	20.18
215	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]	12/2005	702.00 -	755.50	03/2011 -	03/2013	7.62
216	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN - [N25000048]	03/2009	3,500.00 -	4,150.00	01/2012 -	08/2013	18.57
217	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053]	10/2010	966.46 -	994.82	02/2014 -	04/2014	2.93
218	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]	03/2007	245.67 -	373.22	04/2009 -	02/2011	51.92
	Total		8,628.97 -	391,750.50			
	<u>STEEL</u>						
219	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]	10/2005	8,692.00 -	12,291.00	10/2009 -	07/2014	41.41
220	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]	01/2007	295.89 -	607.17	12/2011 06/2010	01/2015	105.20
221	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]	06/2006	108.00 -	216.68	09/2008 -	04/2014	100.63
222	EXPANSION OF IISCO STEEL PLANT - [N12000051]	06/2008	14,443.00 -	16,408.00	12/2011 -	06/2014	13.61
223	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT EXP. UNIT - [N12000068]	07/2007	202.00 -	343.58	01/2010 -	11/2013	70.09
224	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]	08/2006	260.00 -	349.64	12/2009 -	06/2013	34.48
225	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079]	06/2012	237.09 -	254.90	12/2014 -	12/2014	7.51
226	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]	11/2012	313.05 -	339.35	06/2015 -	06/2015	8.40
	Total		24,551.03 -	422,560.82			

(March 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>TELECOMMUNICATIONS</u>						
227	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTARANCHAL [N26000058]	01/2009	149.15 -	158.72	06/2009 -	06/2014	6.42
228	GSM EQUIPMENT OF 799000 LINES (2G) 101000 LINES 3(G) JHARKHAND PHASE V.1 TELECOM CIRCLE [N26000088]	03/2008	328.13 -	392.13	03/2009 -	01/2013	19.50
229	GSM EQUIPMENT OF 1625000 LINES (2G) 325000 LINES 3(G) MP PHASE V.1 TELECOM CIRCLE [N26000090]	11/2009	916.70 -	930.60	11/2010 -	09/2013	1.52
	Total		1,393.98 -	424,042.27			
	<u>URBAN DEVELOPMENT</u>						
230	BANGALORE METRO RAIL PROJECT - [N28000008]	05/2006	6,395.00 -	11,609.00	06/2011 -	03/2013	81.53
231	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX, MUMBAI - [N28000048]	11/2006	114.18 173.08	173.08	04/2009 -	-	51.59
	Total		6,509.18 -	435,824.35			
	<u>WATER RESOURCES</u>						
232	PAGLADIYA DAM PROJECT - [300100001]	01/2001	542.90 -	1,187.00	12/2007 -	12/2012	118.64
	Total		542.90 -	437,011.35			
	Grand Total		252,478.71	3,356,784.43			

(March 2014)

					Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	T.O.R (in months)
1	2	3	4	5	6	7	8	9
15	WAX PROJECT - [N16000101]	06/2010	576.60 -	676.05	12/2013 -	03/2014	17.25	3
16	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]	01/2006	672.00 -	1,038.00	10/2011 -	09/2014	54.46	35
17	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]	01/2006	732.00 -	1,227.00	10/2011 -	06/2015	67.62	44
18	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	06/2015	70.49	41
19	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]	06/2007	1,436.21 1,456.96	1,456.96	07/2010 05/2012	05/2014	1.44	46
20	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]	01/2010	2,163.64 -	2,331.62	06/2012 -	05/2014	7.76	23
21	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]	01/2007	2,323.40 -	2,920.82	09/2010 03/2012	12/2015	25.71	63
22	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]	08/2006	3,195.16 -	3,690.37	12/2008 -	09/2014	15.50	69
23	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]	03/2010	3,241.03 -	6,638.94	03/2013 -	11/2014	104.84	20
24	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]	06/2007	3,248.78 -	5,633.44	08/2010 03/2012	05/2014	73.40	45
25	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]	10/2007	5,713.03 -	8,813.41	05/2010 -	05/2014	54.27	48
26	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00 -	32,710.00	11/2012 -	12/2014	9.85	25
	Total		55,437.09 -	115,508.32				
	POWER							
27	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	951.48	07/2013 -	11/2014	126.00	16
28	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,128.38	08/2013 -	09/2015	96.59	25
29	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]	09/2005	1,061.38 -	1,501.75	09/2009 -	07/2015	41.49	70
30	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	07/2010 -	02/2017	79.77	79
31	KISHANGANGA HEP - [N18000031]	07/2007	2,238.67 -	3,642.00	01/2016 -	11/2016	62.69	10
32	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]	10/2005	2,304.56 -	2,716.00	10/2010 -	08/2014	17.85	46
33	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]	08/2008	2,360.95 -	2,580.90	08/2012 -	03/2014	9.32	19
34	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,745.08	07/2014 -	07/2018	50.31	48
35	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	4,653.95	12/2009 06/2016	03/2017	86.39	87

(March 2014)

					Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	T.O.R (in months)
1	2	3	4	5	6	7	8	9
36	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014	11/2006	2,978.48 -	3,846.30	03/2013 -	03/2017	29.14	48
37	PARBATI HEP (NHPC) II - [180100210	09/2002	3,919.59 -	5,366.00	09/2009 -	07/2018	36.90	106
38	KOLDAM HEP (NTPC) - [180100211	10/2002	4,527.15 -	7,220.00	04/2009 -	05/2015	59.48	73
39	SUBANSIRI LOWER H.E.P (NHPC) - [180100221	09/2003	6,285.33 -	10,667.00	09/2010 -	07/2018	69.71	94
40	BARH STPP(3X660MW) NTPC - [180100242	12/2003	8,692.97 -	8,693.00	12/2009 -	03/2017	0.00	87
	Total		42,009.56 -	175,199.02				
	<u>RAILWAYS</u>							
41	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	31.42 154.30	445.40	03/2007 03/2007	03/2015	1,317.57	96
42	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	100.00 -	725.53	12/2010 -	03/2015	625.53	51
43	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	12/2009 -	03/2014	300.67	51
44	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	1,423.98	03/2005 12/2008	12/2016	1,172.55	141
45	ETAWAH-MAINPURI (NL),NCR - [220100318	09/2001	120.00 -	245.39	12/2008 -	09/2014	104.49	69
46	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	276.00	03/2009 03/2009	08/2014	106.88	65
47	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163	04/2010	146.95 -	171.02	06/2013 -	06/2014	16.38	12
48	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION [N22000162	04/2010	149.90 -	177.38	03/2015 -	12/2015	18.33	9
49	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	288.00	02/2009 02/2009	08/2014	73.33	66
50	ELECTRIFICATION OF KHURJA-MEERUT- SAHARANPUR AND G'BAD-MEERUT - [N22000094	02/2008	171.10 -	246.44	03/2012 -	03/2014	44.03	24
51	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045	03/1997	186.92 -	261.70	02/2006 -	06/2015	40.01	112
52	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	596.36	06/2004 -	12/2014	207.29	126
53	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097	03/1984	293.97 -	1,074.45	06/2005 -	06/2016	265.50	132
54	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	04/2006	325.00 -	1,116.53	03/2010 -	03/2017	243.55	84
55	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	401.81 -	1,814.10	03/2004 -	12/2014	351.48	129
56	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107	04/2007	482.00 -	482.70	03/2013 -	03/2014	0.15	12

(March 2014)

					Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	T.O.R (in months)
1	2	3	4	5	6	7	8	9
57	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]	03/1984	520.00 422.79	835.04	03/1995 -	03/2015	60.58	240
58	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,393.48	04/2014 -	03/2017	286.46	35
59	PATNA GANGA BRIDGE (NL), ECR - [220100308]	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76	98
60	HYDERABAD/SECUNDERABD MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II - [N22000213]	04/2012	632.68 -	816.55	04/2012 -	03/2016	29.06	47
61	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41	69
62	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	4,478.17	03/2011 -	03/2017	515.51	72
63	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	1,655.81	12/2008 -	03/2018	125.90	111
64	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	1,141.75	03/2014 -	03/2017	40.38	36
65	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA [N22000194]	04/1999	895.00 -	1,091.98	03/2007 -	03/2017	22.01	120
66	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]	04/2002	921.00 -	2,363.00	03/2009 -	12/2014	156.57	69
67	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]	09/1997	1,000.00 -	4,500.00	04/2008 12/2011	12/2017	350.00	116
68	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	3,380.58	12/2015 -	03/2017	152.38	15
69	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	4,184.84	03/2009 -	03/2017	149.65	96
70	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	20,000.00	11/2002 -	12/2017	700.00	181
71	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	6,213.84	03/2014 -	12/2016	17.24	33
	Total		22,111.99 -	241,752.76				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
72	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	241.28	11/2008 -	12/2014	55.62	73
73	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 [240106279]	12/2003	167.64 -	265.63	11/2008 -	12/2014	58.45	73
74	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	04/2014	68.99	57
75	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	382.02	04/2009 -	12/2014	91.19	68
76	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]	12/2003	200.00 -	247.43	04/2009 -	12/2014	23.72	68
77	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061]	12/2003	212.00 -	333.83	09/2007 -	05/2014	57.47	80

(March 2014)

					Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	T.O.R (in months)
1	2	3	4	5	6	7	8	9
78	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063	12/2003	217.61 -	309.56	04/2010 -	01/2016	42.25	69
79	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 -	361.00	02/2009 -	05/2014	28.93	63
	Total		1,628.10 -	244,224.74				
	<u>SHIPPING AND PORTS</u>							
80	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) [N25000035	10/2002	150.00 -	600.00	03/2006 -	06/2014	300.00	99
81	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053	10/2010	966.46 -	994.82	02/2014 -	04/2014	2.93	2
82	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL [N25000016	11/2007	1,228.00 -	2,158.16	12/2010 -	10/2015	75.75	58
	Total		2,344.46 -	247,977.72				
	<u>STEEL</u>							
83	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038	06/2006	108.00 -	216.68	09/2008 -	04/2014	100.63	67
84	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018	01/2007	295.89 -	607.17	12/2011 06/2010	01/2015	105.20	37
85	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067	10/2005	8,692.00 -	12,291.00	10/2009 -	07/2014	41.41	57
86	EXPANSION OF IISCO STEEL PLANT - [N12000051	06/2008	14,443.00 -	16,408.00	12/2011 -	06/2014	13.61	30
	Total		23,538.89 -	277,500.57				
	<u>TELECOMMUNICATIONS</u>							
87	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTANCHAL [N26000058	01/2009	149.15 -	158.72	06/2009 -	06/2014	6.42	60
	Total		149.15 -	277,659.29				
	Grand Total		173,345.02	1,668,939.43				

List of Projects Ahead of Schedule w.r.t. Latest Schedule

						(March 2014)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>POWER</u>						
1	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID [N16000144]	9/2012	1,508.74	1,508.74	247.12	06/2016 -	12/2015
	Total		1,508.74 -	1,508.74	247.12		
	<u>PETROLEUM</u>						
2	LPG TERMINAL AT KOCHI - [N16000171]	12/2012	607.06 -	607.06	20.38	01/2016 -	12/2015
	Total		607.06 -	607.06	20.38		
	<u>POWER</u>						
3	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID [N18000137]	9/2012	1,935.35 -	1,935.35	605.31	12/2014 -	11/2014
	Total		1,935.35 -	1,935.35	605.31		
	Grand Total		4,051.15	4,051.15	872.81		

List of Projects on schedule w.r.t. Latest Schedule

(March 2014)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
1	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]	2/2011	452.00 -	452.00	230.42	03/2015 -	03/2015
2	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]	10/2012	217.60 -	217.60	0.04	03/2015 -	03/2015
	Total		669.60 -	669.60	230.46		
	<u>COAL</u>						
3	KUSMUNDA EXPN.OCP(SECL)(10-15)MTY - [N06000008]	6/2008	1,188.31 -	7,612.33	747.82	03/2013 03/2023	03/2023
4	BINA EXTN. PROJ(6.0 MTPA) - [N06000019]	11/2006	168.97 -	168.97	44.08	03/2014 -	03/2014
5	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]	12/2009	1,352.04 -	1,143.54	613.44	03/2016 03/2016	03/2016
6	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]	6/2011	746.04 -	535.10	222.53	03/2015 -	03/2015
7	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.00 -	490.10	160.06	03/2017 -	03/2017
8	TALABIRA OCP - [N06000043]	3/2008	447.72 -	447.72	50.46	03/2016 -	03/2016
9	BATURA OCP (2.0 MTY) - [N06000049]	9/2008	203.82 -	203.82	-	03/2015 -	03/2015
10	MURADH UG TURN-KEY PROJECT - [N06000096]	2/2011	339.88 -	339.88	-	04/2014 -	04/2014
11	JALAGAM VENGALA RAO OCP-II - [N06000094]	7/2011	447.06 -	447.06	29.04	03/2015 -	03/2015
12	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	7/2011	162.76 -	162.76	2.56	03/2015 -	03/2015
13	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	19.19	03/2018 -	03/2018
14	KISTARAM OCP - [N06000089]	11/2010	242.29 -	242.29	-	03/2015 -	03/2015
15	KARMA OCP (1.0MTY) - [N06000088]	6/2009	162.46 -	162.46	55.85	03/2014 -	03/2014
16	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]	12/2009	510.85 -	510.85	268.01	03/2016 -	03/2016
17	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	90.43	03/2016 -	03/2016

(March 2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
18	RKP OCP PHASE-I - [N06000079]	3/2010	209.78 -	209.78	93.46	03/2015 -	03/2015
19	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.33 -	610.33	-	03/2022 -	03/2022
20	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	67.22	03/2020 -	03/2020
21	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.14 -	430.14	65.48	03/2016 -	03/2016
22	KALYANIKHANI OPENCAST PROJECT - [N06000101]	7/2012	417.33 -	417.33	0.24	07/2016 -	07/2016
23	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]	6/2012	365.01 -	365.01	5.43	06/2015 -	06/2015
24	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]	4/2012	258.56 -	258.56	55.25	03/2016 -	03/2016
25	MOONIDIH XV SEAM UG - [N06000098]	8/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015
26	PELMA OCP(10.00MTY) - [N06000045]	7/2008	448.32 -	448.32	-	03/2015 -	03/2015
27	GOPAL PRASAD OCP (15MTY) - [N06000042]	2/2008	395.87 -	395.87	75.42	03/2015 -	03/2015
	Total		12,967.79 -	19,020.47	2,665.97		
	<u>PETROLEUM</u>						
28	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]	3/2010	3,241.03 -	6,638.94	1,451.42	03/2013 11/2014	11/2014
29	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]	3/2012	5,608.40 -	5,608.40	2,182.76	05/2015 -	05/2015
30	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]	4/2012	600.17 -	600.17	219.43	12/2014 -	12/2014
31	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	522.90	03/2015 -	03/2015
32	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	3/2011	861.79 -	861.79	495.39	05/2013 06/2014	06/2014
33	PIPELINE REPLACEMENT PROJECT-3 - [N16000137]	4/2012	2,547.26 -	2,547.26	1,015.93	05/2014 -	05/2014
34	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	11/2012	666.00 -	701.00	202.33	11/2015 -	11/2015
35	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]	4/2013	284.82 -	284.82	-	04/2015 -	04/2015
36	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	5/2013	4,124.35 -	4,124.35	-	04/2016 -	04/2016
37	KOTA JOBNER PIPELINE PROJECT - [N16000170]	4/2011	276.26 -	276.26	135.34	03/2015 -	03/2015
38	MARKETING TERMINAL AT PARADEEP - [N16000168]	7/2009	199.75 -	199.75	133.42	06/2014 -	06/2014

(March 2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
39	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]	3/2013	1,138.50 -	1,138.50	33.92	04/2015 -	04/2015
40	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]	12/2012	3,513.07 -	3,513.07	-	02/2016 -	02/2016
41	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]	9/2011	202.25 -	202.25	33.26	07/2016 -	07/2016
42	MOUNDED BULLET PROJECT AT CPCL - [N16000154]	12/2012	279.00 -	279.00	65.09	12/2014 -	12/2014
43	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]	8/2011	586.00 -	586.00	160.16	08/2015 -	08/2015
44	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]	2/2011	913.00 -	913.00	106.53	07/2015 -	07/2015
45	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	9/2012	871.35 -	871.35	10.93	03/2015 -	03/2015
46	REWARI KANPUR PIPELINE PROJECT - [N16000145]	2/2012	1,210.64 -	1,210.64	504.90	11/2015 -	11/2015
	Total		29,183.27 -	33,222.20	7,273.71		
	<u>POWER</u>						
47	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,128.38	811.78	08/2013 09/2015	09/2015
48	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNAM OF ANDHRA PRADESH(PGCIL) - [N18000111]	8/2011	1,637.34 -	1,637.34	1,353.68	08/2014 -	08/2014
49	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]	11/2011	2,127.51 -	2,127.51	-	07/2014 -	07/2014
50	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]	5/2011	1,961.87 -	1,961.87	-	05/2014 -	05/2014
51	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]	3/2011	2,569.25 -	2,569.25	-	03/2014 -	03/2014
52	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	297.33	214.02	08/2014 -	08/2014
53	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	1/2011	913.63 -	913.63	573.22	07/2006 12/2015	12/2015
54	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]	2/2014	167.40 -	167.40	-	12/2015 -	12/2015
55	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]	2/2014	243.53 -	243.53	-	08/2014 -	08/2014
56	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	2/2014	908.08 -	908.08	-	06/2016 -	06/2016
57	KUDGI STPP STAGE 1 - [N18000131]	12/2011	15,166.19 -	15,166.19	3,237.00	12/2016 -	12/2016

(March 2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
58	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]	6/2012	1,263.26 -	1,263.26	598.85	11/2014 -	11/2014
59	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]	11/2011	723.63 -	723.63	314.55	11/2014 -	11/2014
60	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]	12/2011	901.77 -	901.77	598.30	08/2014 -	08/2014
61	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]	3/2012	206.44 -	206.44	42.57	06/2014 -	06/2014
62	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]	3/2012	198.63 -	198.63	-	09/2014 -	09/2014
63	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]	2/2012	1,927.16 -	1,927.16	906.91	10/2014 -	10/2014
64	TRANSMISSION SYS ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1 - [N18000121]	2/2012	324.33 -	324.33	141.27	08/2014 -	08/2014
65	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]	2/2012	1,310.85 -	1,310.85	-	02/2015 -	02/2015
66	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	3/2013	514.20 -	514.20	-	06/2015 -	06/2015
67	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	64.00	08/2017 -	08/2017
68	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	11/2012	11,846.00 -	11,846.00	1,321.00	05/2017 -	05/2017
69	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139]	1/2013	182.80 -	182.80	10.71	10/2014 -	10/2014
70	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]	12/2012	156.04 -	156.04	24.39	10/2014 -	10/2014
71	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]	9/2012	803.34 -	803.34	211.42	03/2015 -	03/2015
72	VINDHYACHAL STPP STAGE-V - [N18000134]	12/2011	3,180.40 -	3,180.40	881.00	08/2015 -	08/2015
73	SOLAPUR STPP - [N18000133]	3/2012	9,395.18 -	9,395.18	2,085.00	11/2016 -	11/2016
74	MOUDA STPP STAGE 2 - [N18000132]	3/2012	7,921.47 -	7,921.47	1,878.00	09/2016 -	09/2016
75	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]	2/2014	539.82 -	539.82	-	06/2016 -	06/2016
76	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]	1/2014	374.63 -	374.63	-	04/2016 -	04/2016

(March 2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
77	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,364.52	-	05/2016 -	05/2016
78	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154]	10/2013	1,315.90 -	1,315.90	-	11/2016 -	11/2016
79	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]	9/2013	1,575.30 -	1,575.30	-	05/2016 -	05/2016
80	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]	9/2013	680.69 -	680.69	-	03/2016 -	03/2016
81	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	2/2013	11,638.55 -	11,638.55	1,030.00	09/2017 -	09/2017
82	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]	6/2012	1,909.24 -	1,909.24	381.51	06/2015 -	06/2015
83	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]	3/2013	2,514.88 -	2,514.88	23.38	12/2015 -	12/2015
84	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]	1/2012	1,422.85 -	1,422.85	633.79	01/2015 -	01/2015
	Total		92,285.00 -	92,839.39	17,336.35		
	<u>RAILWAYS</u>						
85	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	4/1998	183.23 -	818.29	111.78	02/2015 -	02/2015
86	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	4/2010	2,619.02 -	2,913.51	398.86	03/2016 -	03/2016
87	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	4/2010	3,951.98 -	3,951.98	308.18	03/2016 -	03/2016
88	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	4/2006	325.00 -	1,116.53	277.91	03/2010 03/2017	03/2017
89	HIMMATNAGAR - UDAIPUR GAUGE CONVERSION (NWR) - [N22000112]	4/2008	829.74 -	829.74	53.05	03/2015 -	03/2015
90	SURATPURA - HANUMANGARH - SRIGANGANAGAR GAUGE CONVERSION (NWR) - [N22000114]	4/2008	516.23 -	516.23	478.66	03/2014 -	03/2014
91	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	3/2013	4,874.58 -	4,874.58	-	03/2016 -	03/2016
92	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	4/2010	423.66 -	423.66	158.41	03/2017 -	03/2017
93	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI- JONGALPARA-FURFURA SHARIF NL - [N22000244]	4/2009	257.42 -	257.42	34.36	03/2014 -	03/2014

(March 2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
94	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	4/2011	299.60 -	299.60	1.10	03/2017 -	03/2017
95	PLASSEY-JIAGANJ DOUBLING - [N22000220]	4/2011	248.07 -	248.07	12.05	03/2015 -	03/2015
96	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	4/2010	309.44 -	388.67	74.58	12/2015 -	12/2015
97	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]	4/2010	622.41 -	2,030.50	1.60	02/2019 -	02/2019
98	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	1,176.09 -	3,845.60	1.92	02/2020 -	02/2020
99	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]	4/2008	1,389.62 -	1,389.62	796.60	03/2014 -	03/2014
100	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	4/2008	653.19 -	653.47	277.38	03/2014 -	03/2014
	Total		18,679.28 -	24,557.47	2,986.44		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
101	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	382.02	107.55	04/2009 12/2014	12/2014
102	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]	12/2003	167.64 -	265.63	92.14	11/2008 12/2014	12/2014
103	GUWHATI TO NALBARI (AS-4) - [N24000038]	12/2003	175.96 -	175.96	249.37	04/2008 01/2015	01/2015
104	GUWAHATI TO NALBARI (AS-5) - [N24000046]	12/2003	198.16 -	198.16	306.31	04/2008 01/2015	01/2015
105	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 -	208.00	313.93	04/2008 01/2015	01/2015
106	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	306.32	04/2010 01/2016	01/2016
107	4 LANING OF NAGPUR-BETUL - [N24000155]	2/2011	2,498.76 -	2,498.76	2,425.10	08/2014 -	08/2014
108	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	1,928.22	428.98	04/2015 -	04/2015
109	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	61.44	12/2015 -	12/2015
110	2 LANING WITH PS KANPUR KABRAI - [N24000221]	1/2013	373.47 -	373.47	43.77	07/2014 -	07/2014
111	2 LANING WITH PS AGRA ALIGARH - [N24000220]	10/2012	250.50 -	250.50	328.56	10/2014 -	10/2014
112	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	37.66	09/2015 -	09/2015
113	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]	2/2013	1,232.00 -	1,232.00	252.60	08/2015 -	08/2015
114	PANVEL-INDAPUR - [N24000216]	12/2011	942.69 -	942.69	264.53	06/2014 -	06/2014

(March 2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
115	RANCHI-RARGA-JAMSETHPUR - [N24000215]	12/2012	1,479.00 -	1,479.00	285.46	06/2015 -	06/2015
116	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]	4/2012	624.00 -	624.00	424.10	04/2014 -	04/2014
117	BARSAT-KRISHNANAGAR - [N24000229]	8/2012	867.00 -	867.00	598.56	02/2015 -	02/2015
118	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]	6/2013	1,287.95 -	1,287.95	52.18	11/2015 -	11/2015
119	REENGUS SIKAR - [N24000227]	3/2012	333.51 -	333.51	260.16	09/2014 -	09/2014
120	2-LANING WITH PAVED SHOULDERS OF MULTAI CHHINDWARA SEONI SEC [N24000226]	10/2011	1,565.00 -	1,565.00	1,119.27	10/2014 -	10/2014
121	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]	3/2012	828.00 -	828.00	582.60	09/2014 -	09/2014
122	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI [N24000211]	7/2012	356.40 -	356.40	42.51	07/2014 -	07/2014
123	NAGPUR-WAINGANGA BRIDGE - [N24000210]	4/2012	484.19 -	484.19	283.53	10/2014 -	10/2014
124	KRISHNANAGAR-BERHAMPUR - [N24000209]	2/2012	702.16 -	702.16	651.04	07/2014 -	07/2014
125	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]	4/2012	1,396.18 -	1,396.18	1,383.05	09/2014 -	09/2014
126	SIX LANING OF CHANDIKHOL-JAGATPUR- BHUBANESWAR [N24000205]	12/2011	1,047.00 -	1,047.00	234.03	06/2014 -	06/2014
127	BEAWAR-PALI-PINDWARA - [N24000199]	12/2011	2,388.00 -	2,388.00	1,846.87	06/2014 -	06/2014
128	PANIKHOLI-RIMOLI - [N24000197]	3/2012	1,410.00 -	1,410.00	158.91	09/2014 -	09/2014
129	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]	11/2011	909.00 -	909.00	959.15	05/2014 -	05/2014
130	2LANING WITH PS GOPALGANJ-CHAPPRA - [N24000190]	12/2011	325.00 -	325.00	166.73	05/2014 -	05/2014
131	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]	10/2011	375.09 -	375.09	174.34	04/2014 -	04/2014
132	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]	9/2011	574.00 -	574.00	794.16	03/2014 -	03/2014
133	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 [N24000183]	11/2011	1,535.00 -	1,535.00	1,328.51	05/2014 -	05/2014
134	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]	9/2011	2,848.00 -	2,848.00	993.84	03/2014 -	03/2014
135	GHAZIABAD-ALIGARH NH-91 - [N24000170]	2/2011	1,141.00 -	1,141.00	1,319.54	08/2013 06/2014	06/2014
136	NASHRI CHANANI - [N24000162]	6/2010	2,159.00 -	2,159.00	374.22	06/2015 -	06/2015
137	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]	7/2010	1,987.00 -	1,987.00	1,080.00	07/2015 -	07/2015

(March 2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
138	PANIPAT-ROHTAK - [N24000151]	4/2011	807.00 -	807.00	1,325.75	10/2014 -	10/2014
139	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]	12/2003	160.00 -	160.00	209.92	05/2008 07/2014	07/2014
140	NALBARI TO BIJNI (AS-6) - [N24000047]	12/2003	225.00 -	225.00	269.79	06/2008 05/2014	05/2014
141	SONAPUR TO GUWAHTI (AS-3) - [N24000044]	12/2003	245.00 -	245.00	491.20	03/2008 01/2015	01/2015
142	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	241.28	151.77	11/2008 12/2014	12/2014
143	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]	12/2003	200.00 -	247.43	180.36	04/2009 12/2014	12/2014
	Total		40,504.58 -	41,010.40	22,959.81		
	<u>SHIPPING AND PORTS</u>						
144	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) [N25000035]	10/2002	150.00 -	600.00	139.80	03/2006 06/2014	06/2014
145	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053]	10/2010	966.46 -	994.82	427.54	02/2014 04/2014	04/2014
146	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY - [N25000062]	1/2012	511.87 -	511.87	106.72	03/2014 08/2014	08/2014
	Total		1,628.33 -	2,106.69	674.06		
	<u>STEEL</u>						
147	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]	1/2007	295.89 -	607.17	369.58	12/2011 01/2015	01/2015
148	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]	4/2011	572.00 -	572.00	379.62	04/2013 09/2014	09/2014
149	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]	2/2011	898.55 -	898.55	291.82	05/2013 01/2015	01/2015
150	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH - [N12000078]	7/2012	332.65 -	332.65	102.39	08/2014 -	08/2014
151	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079]	6/2012	237.09 -	254.90	31.93	12/2014 -	12/2014
152	REBUILDING OF BATTERY BLOCK 5A AND RE- CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]	11/2012	313.05 -	339.35	83.98	06/2015 -	06/2015
153	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]	10/2012	160.48 -	160.48	18.86	09/2014 -	09/2014
154	REBUILDING OF COB-7 AT BSL - [N12000083]	10/2013	245.67 -	245.67	6.91	05/2016 -	05/2016

(March 2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		3,055.38 -	3,410.77	1,285.09		
	<u>URBAN DEVELOPMENT</u>						
155	DELHI MRTS PHASE-III - [N28000056	9/2011	38,585.00 -	38,585.00	7,107.57	03/2016 -	03/2016
156	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058	2/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019
	Total		64,990.14 -	64,990.14	7,107.57		
	Grand Total		263,963.37	281,827.13	62,519.46		

List of Delayed Projects w.r.t. Latest Schedule

(March 2014)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00 -	17,270.00	17,198.00	12/2008 -	12/2014	72	-
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 -	5,677.00	-	09/2010 -	03/2015	54	-
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	-	12/2015 -	11/2016	11	-
4	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	-	12/2016 -	03/2017	3	-
	Total		40,442.00 -	46,726.00	17,198.00				
	<u>CIVIL AVIATION</u>								
5	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 335.61	388.53	278.32	05/2012 -	04/2014	23	-
6	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	344.28	-	03/2014 -	10/2014	7	-
7	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	309.46	269.55	01/2011 04/2013	03/2015	50	23
	Total		989.35 -	1,042.27	547.87				
	<u>COAL</u>								
8	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	471.66 341.63	341.63	119.71	03/2011 -	03/2014	36	-
9	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,UTTAR PRADESH	06/2011	789.88 -	741.62	388.56	03/2013 -	03/2014	12	-
10	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,TAMIL NADU	10/2004	2,030.78 3,027.59	3,027.59	2,904.44	06/2009 -	06/2014	60	-
11	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	5,191.62	03/2012 -	08/2014	29	-
12	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,ANDHRA PRADESH	12/2009	212.34 1,228.39	1,228.39	1,206.66	03/2013 09/2012	03/2015	24	30
13	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 -	259.40	6.99	03/2012 -	03/2015	36	-
14	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	116.72	03/2013 -	03/2015	24	-
15	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.63 -	479.63	120.15	03/2013 -	03/2015	24	-
16	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,ANDHRA PRADESH	12/2009	418.97 -	418.97	240.26	03/2012 -	03/2015	36	-
17	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,ANDHRA PRADESH	03/2010	181.19 -	181.19	35.35	03/2012 -	03/2015	36	-
18	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	123.07	03/2013 -	03/2015	24	-

(March 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
19	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL, CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,632.11	03/2014 -	03/2016	24	-
20	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL, CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,345.03	03/2014 -	03/2016	24	-
21	MAGADH OC 20 MTY (CCL) - [N06000015]CCL, JHARKHAND	08/2008	469.78 -	706.40	32.17	07/2012 -	03/2016	44	-
22	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]MCL, ODISHA	12/2007	172.08 -	172.08	131.62	03/2010 -	03/2016	72	-
23	CHURCHA ROUG (1.35 MTY) - [N06000046]SECL, CHHATISGARH	06/2008	462.35 -	462.35	270.85	03/2014 -	03/2016	24	-
24	KAKATIYA LONGWALL - [N06000048]SCCL, ANDHRA PRADESH	12/2008	453.63 -	453.63	102.23	12/2012 -	03/2016	39	-
25	RAJMAHAL OC EXP. - [N06000056]ECL, JHARKHAND	09/2009	153.82 -	153.82	33.46	03/2014 -	03/2016	24	-
26	PENGANGA OC - [N06000066]WCL, MAHARASHTRA	10/2008	339.77 -	339.77	2.30	03/2014 -	03/2016	24	-
27	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL, ODISHA	08/2008	207.28 -	207.28	126.88	03/2012 -	03/2016	48	-
28	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24	-
29	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH	12/2009	321.42 -	321.50	213.59	03/2014 -	03/2016	24	-
30	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL, JHARKHAND	08/2007	163.51 -	163.51	35.38	03/2011 -	03/2016	60	-
31	TAPIN OCP (2.5 MTY) - [N06000086]CCL, JHARKHAND	08/2008	264.68 -	264.68	141.89	03/2012 -	03/2016	48	-
32	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL, ODISHA	01/2005	302.96 -	302.96	118.59	03/2010 -	03/2017	84	-
33	JHANJRA R-VI SEAM PSLW - [N06000020]ECL, WEST BENGAL	11/2006	287.18 -	287.17	36.31	03/2011 -	03/2017	72	-
34	JAGANNATHPOR OC - [N06000075]SECL, CHHATISGARH	09/2008	152.43 -	152.43	-	03/2015 -	03/2017	24	-
35	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL, JHARKHAND	12/2007	179.87 -	179.87	63.66	03/2012 -	03/2017	60	-
36	NEYVELI NEW THERMAL POWER PROJECT (2X500 MW) - [N06000095]NLC, TAMIL NADU	06/2011	5,907.11 -	5,907.11	339.15	12/2015 -	04/2018	28	-
	Total		25,052.78 -	28,822.24	15,078.75				
	STEEL								
37	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL, JHARKHAND	05/2010	6,325.00 -	6,325.00	4,591.34	12/2011 -	03/2014	27	-
38	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL, ANDHRA PRADESH	06/2006	108.00 216.68	216.68	160.46	09/2008 12/2013	04/2014	67	4
39	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL, WEST BENGAL	06/2008	14,443.00 -	16,408.00	15,787.87	12/2011 -	06/2014	30	-
40	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL, ANDHRA PRADESH	10/2005	8,692.00 12,291.00	12,291.00	10,792.31	10/2009 10/2012	07/2014	57	21
41	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]RINL, MULTI STATE	07/2007	480.00 -	450.00	309.45	09/2009 05/2012	07/2014	58	26

(March 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
42	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA	12/2011	187.33 -	187.33	119.88	10/2013 -	08/2014	10	-
43	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]SAIL,ODISHA	08/2010	11,812.00 -	11,812.00	10,870.17	03/2013 -	09/2014	18	-
44	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,WEST BENGAL	08/2010	2,875.00 -	2,875.00	2,153.22	12/2012 -	12/2014	24	-
45	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	12,491.86	03/2013 -	03/2015	24	-
46	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL,ODISHA	11/2011	254.55 -	254.55	104.16	11/2013 -	06/2015	19	-
	Total		62,441.88 -	68,084.56	57,380.72				
	<u>PETROLEUM</u>								
47	WAX PROJECT - [N16000101]NRL,ASSAM	06/2010	576.60 -	676.05	511.99	12/2013 -	03/2014	3	-
48	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,MAHARASHTRA	06/2007	3,248.78 5,633.44	5,633.44	5,190.51	08/2010 03/2012	05/2014	45	26
49	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,MAHARASHTRA	10/2007	5,713.03 8,813.41	8,813.41	7,351.12	05/2010 03/2013	05/2014	48	14
50	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,MAHARASHTRA	06/2007	1,436.21 1,456.96	1,456.96	1,100.32	07/2010 05/2012	05/2014	46	24
51	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,MAHARASHTRA	01/2009	7,133.39 -	7,133.39	5,543.40	09/2012 -	05/2014	20	-
52	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,MULTI STATE	01/2010	2,163.64 2,331.62	2,331.62	1,889.99	06/2012 -	05/2014	23	-
53	FIRE WATER NETWORK AT URAN - [N16000141]ONGC,MAHARASHTRA	05/2010	171.68 -	171.68	96.43	06/2013 -	05/2014	11	-
54	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]ONGC,TRIPURA	07/2008	288.04 288.04	253.66	210.07	08/2012 -	06/2014	22	-
55	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,MULTI STATE	08/2010	8,140.00 -	8,140.00	6,422.66	02/2014 -	06/2014	4	-
56	POLYPROPYLENE UNIT - [N16000113]MANGALORE REFIN,KARNATAKA	05/2009	1,803.78 -	1,803.78	884.59	07/2012 -	06/2014	23	-
57	MRPL PHASE-III EXPANSION - [N16000114]MANGALORE REFIN,KARNATAKA	08/2008	12,412.00 -	12,160.26	11,518.36	01/2012 -	06/2014	29	-
58	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]BPCL,MAHARASHTRA	08/2009	246.81 -	276.83	258.57	04/2012 -	06/2014	26	-
59	GAS TURBINE GENERATION SET - [N18000146]OIL,ASSAM	07/2009	216.88 -	216.88	177.92	10/2011 -	06/2014	32	-
60	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,ASSAM	08/2008	144.02 -	204.29	154.08	06/2012 -	06/2014	24	-
61	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,ANDHRA PRADESH	03/2009	3,597.00 2,730.00	2,730.00	2,061.74	09/2011 03/2012	07/2014	34	28
62	102 MW WIND POWER PROJECT - [N16000119]ONGC,RAJASTHAN	07/2010	1,106.00 -	678.02	77.45	06/2012 -	07/2014	25	-
63	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,MAHARASHTRA	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	09/2014	69	17

(March 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
64	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC,MULTI STATE	11/2010	331.20 -	331.20	164.19	08/2013 -	09/2014	13	-
65	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,ANDHRA PRADESH	01/2006	672.00 1,038.00	1,038.00	936.55	10/2011 -	09/2014	35	-
66	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,HARYANA	11/2007	281.07 -	281.07	4.42	10/2010 -	12/2014	50	-
67	PARADIP REFINERY PROJECT - [N16000058]IOCL,ODISHA	02/2009	29,777.00 -	32,710.00	25,230.00	11/2012 -	12/2014	25	-
68	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,MAHARASHTRA	03/2009	3,284.00 2,174.00	2,174.00	1,881.89	09/2011 05/2012	12/2014	39	31
69	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	736.65	448.92	09/2011 -	12/2014	39	-
70	CONSTRUCTION OF SIX EFFLUENT TREATMENT PLANTS (ETP), AHMEDABAD AND ANKLESWAR - [N16000099]ONGC,GUJARAT	03/2009	234.78 234.78	317.64	102.78	09/2012 -	12/2014	27	-
71	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	302.26 -	240.95	102.78	09/2012 -	12/2014	27	-
72	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE	01/2012	352.49 -	352.49	84.56	03/2014 -	12/2014	9	-
73	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 -	202.94	2.00	01/2014 -	01/2015	12	-
74	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 -	2,378.89	1,496.19	03/2013 03/2014	03/2015	24	12
75	CONSTRUCTION OF ONE ETP AT GGS-NADA, ANKLESHWAR - [N16000134]ONGC,GUJARAT	10/2011	200.69 -	200.69	8.08	07/2014 -	03/2015	8	-
76	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL,MAHARASHTRA	01/1999	1,419.00 -	1,419.00	409.10	12/2014 -	03/2015	3	-
77	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 -	2,592.17	234.78	05/2014 -	05/2015	12	-
78	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	793.29	10/2011 -	06/2015	44	-
79	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,102.03	01/2012 -	06/2015	41	-
80	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	961.93	09/2012 -	08/2015	35	-
81	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	11/2012	309.81 -	309.82	67.83	10/2014 -	10/2015	12	-
82	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	270.00	-	12/2014 -	10/2015	10	-
83	CONSTRUCTION OF THREE ETPS, MEHSANA - [N16000135]ONGC,GUJARAT	03/2012	260.74 -	260.74	0.52	11/2014 -	11/2015	12	-
84	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,MAHARASHTRA	01/2007	2,323.40 2,920.82	2,920.82	1,915.45	09/2010 03/2012	12/2015	63	45
85	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18 -	7,596.18	13.50	01/2013 -	12/2015	35	-
86	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE	06/2010	2,523.00 -	2,523.00	1,002.33	01/2014 -	12/2015	23	-

(March 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
87	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	330.47	270.05	03/2012 -	03/2016	48	-
88	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL,KERALA	01/1999	14,225.00 -	14,225.00	1,814.37	12/2015 -	05/2016	5	-
89	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,MULTI STATE	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	06/2016	122	48
90	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	723.64	-	03/2013 -	06/2016	39	-
91	AHMEDABAD REDEVELOPMENT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10 -	1,916.10	784.46	12/2014 -	12/2016	24	-
92	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63 -	2,189.63	1,039.42	12/2014 -	12/2016	24	-
93	MEHESANA REDEVELOPMENT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	3,823.00	1,076.07	04/2015 -	03/2017	23	-
94	CREATION OF SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND ETP AT MADHUBAN - [N16000167]OIL,MULTI STATE	08/2006	374.56 -	374.56	10.60	09/2012 -	03/2017	54	-
	Total		135,390.62 -	146,257.94	90,112.20				
	<u>POWER</u>								
95	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]PGCIL,MULTI STATE	08/2008	2,360.95 -	2,580.90	-	08/2012 -	03/2014	19	-
96	765 KV POOLING STATION AND NETWORK WITH DVC AND MAITHOB RBC - [N18000069]PGCIL,MULTI STATE	08/2008	7,075.33 -	7,075.33	-	08/2012 -	03/2014	19	-
97	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 -	2,074.86	-	03/2013 -	03/2014	12	-
98	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19 -	2,743.19	-	12/2013 -	03/2014	3	-
99	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 -	752.64	-	07/2013 -	03/2014	8	-
100	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	633.83	11/2012 -	04/2014	17	-
101	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 -	477.69	471.52	09/2010 -	06/2014	45	-
102	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]PGCIL,MULTI STATE	09/2011	1,366.34 -	1,366.34	952.26	12/2013 -	06/2014	6	-
103	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	393.96	02/2014 -	06/2014	4	-
104	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL,MADHYA PRADESH	03/2012	213.78 -	213.78	103.39	03/2014 -	06/2014	3	-

(March 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
105	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,HIMACHAL PRADESH	10/2005	2,304.56 -	2,716.00	2,349.46	10/2010 -	08/2014	46	-
106	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	487.49	277.05	06/2014 -	09/2014	3	-
107	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 623.44	951.48	745.55	07/2013 -	11/2014	16	-
108	SYSTEM STRENGTHENING IN NR FOR SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	975.26	08/2012 -	12/2014	28	-
109	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,007.98	04/2013 -	12/2014	20	-
110	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,272.71	09/2014 -	12/2014	3	-
111	BARH STPP STAGE -II - [N18000047]NTPC,BIHAR	02/2008	7,341.04 -	7,341.04	6,847.00	08/2013 -	03/2015	19	-
112	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	3,739.68	10/2012 -	03/2015	29	-
113	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. - [N18000076]PGCIL,MULTI STATE	03/2010	4,672.99 -	4,672.99	2,964.78	11/2012 -	03/2015	28	-
114	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	241.16	11/2013 -	03/2015	16	-
115	KOLDAM HEP (NTPC) - [180100211]NTPC,HIMACHAL PRADESH	10/2002	4,527.15 7,220.00	7,220.00	5,687.00	04/2009 -	05/2015	73	-
116	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 -	1,746.65	317.22	08/2014 -	05/2015	9	-
117	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	-	04/2015 -	05/2015	1	-
118	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	7,937.67	08/2013 -	06/2015	22	-
119	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP & BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	1,647.80	12/2012 -	06/2015	30	-
120	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NRWR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	66.52	01/2013 -	06/2015	29	-
121	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NRWR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,182.61	11/2013 -	06/2015	19	-
122	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	808.16	11/2012 -	06/2015	31	-
123	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	963.76	08/2014 -	06/2015	10	-

(March 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
124	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	1,427.54	10/2014 -	06/2015	8	-
125	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC, WEST BENGAL	09/2005	1,061.38 -	1,501.75	1,482.62	09/2009 -	07/2015	70	-
126	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B - [N18000077]PGCIL, WEST BENGAL	04/2010	4,404.57 -	4,404.57	464.43	01/2015 -	12/2015	11	-
127	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL, CHHATTISGARH	03/2012	9,569.76 -	9,569.76	1,577.68	06/2015 -	12/2015	6	-
128	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC, ASSAM	01/2008	4,375.35 -	4,375.35	4,311.00	07/2011 -	08/2016	61	-
129	KISHANGANGA HEP - [N18000031]NHPC, JAMMU AND KASHMIR	07/2007	2,238.67 3,642.04	3,642.00	3,283.02	01/2016 -	11/2016	10	-
130	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL, UTTAR PRADESH	07/2006	1,657.00 2,978.86	2,978.86	692.39	07/2010 02/2016	02/2017	79	12
131	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO, ARUNACHAL PRADESH	12/2004	2,496.90 -	4,653.95	2,816.40	12/2009 06/2016	03/2017	87	9
132	BARH STPP(3X660MW) NTPC - [180100242]NTPC, BIHAR	12/2003	8,692.97 -	8,693.00	9,238.00	12/2009 -	03/2017	87	-
133	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC, UTTARAKHAND	11/2006	2,978.48 -	3,846.30	2,020.00	03/2013 -	03/2017	48	-
134	PARBATI HEP (NHPC) II - [180100210]NHPC, HIMACHAL PRADESH	09/2002	3,919.59 -	5,366.00	4,373.85	09/2009 -	07/2018	106	-
135	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC, ARUNACHAL PRADESH	09/2003	6,285.33 -	10,667.00	6,788.54	09/2010 -	07/2018	94	-
136	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL, UTTARAKHAND	08/2008	2,491.58 -	3,745.08	479.33	07/2014 -	07/2018	48	-
	Total		123,002.82 -	140,129.57	80,541.13				
	<u>RAILWAYS</u>								
137	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR, UTTAR PRADESH	04/1999	108.00 427.21	432.72	399.71	12/2009 03/2011	03/2014	51	36
138	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE, UTTAR PRADESH	02/2008	171.10 224.89	246.44	141.55	03/2012 12/2013	03/2014	24	3
139	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR, KARNATAKA	04/2007	482.00 482.70	482.70	560.17	03/2013 -	03/2014	12	-
140	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER, WEST BENGAL	04/2010	146.95 -	171.02	141.84	06/2013 -	06/2014	12	-
141	RAJATGARH-BARANG(LD), ECOR - [220100286]RVNL, ODISHA	04/1999	166.16 -	288.00	-	02/2009 02/2009	08/2014	66	66
142	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL, ODISHA	04/2000	133.41 207.00	276.00	-	03/2009 03/2009	08/2014	65	65
143	ETAWAH-MAINPURI (NL), NCR - [220100318]NCR, UTTAR PRADESH	09/2001	120.00 245.39	245.39	225.46	12/2008 -	09/2014	69	-

(March 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
144	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	401.81 495.44	1,814.10	369.57	03/2004 12/2010	12/2014	129	48
145	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 194.07	596.36	371.50	06/2004 -	12/2014	126	-
146	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 2,363.00	2,363.00	1,339.96	03/2009 12/2012	12/2014	69	24
147	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 207.52	207.52	191.41	12/2012 -	12/2014	24	-
148	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,MULTI STATE	03/1984	520.00 835.04	835.04	622.92	03/1995 -	03/2015	240	-
149	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]RE,WEST BENGAL	04/1974	31.42 393.46	445.40	179.36	03/2007 03/2007	03/2015	96	96
150	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,BIHAR	09/2001	100.00 492.98	725.53	445.01	12/2010 12/2010	03/2015	51	51
151	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	495.74	264.06	06/2013 06/2013	03/2015	21	21
152	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	186.92 261.70	261.70	72.78	02/2006 -	06/2015	112	-
153	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 2,921.00	2,921.00	2,071.46	10/2007 12/2012	12/2015	98	36
154	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	800.00	-	03/2010 -	12/2015	69	-
155	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	177.38	54.89	03/2015 -	12/2015	9	-
156	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	2,298.42	64.57	03/2014 -	03/2016	24	-
157	HYDERABAD/SECUNDERABD MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II - [N22000213]MRTP,ANDHRA PRADESH	04/2012	632.68 -	816.55	17.37	04/2012 -	03/2016	47	-
158	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 1,013.74	1,074.45	457.52	06/2005 07/2011	06/2016	132	59
159	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL,WEST BENGAL	04/2010	2,397.72 -	2,397.72	78.35	03/2016 -	06/2016	3	-
160	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,WEST BENGAL	03/1998	111.90 1,039.29	1,423.98	478.50	03/2005 12/2008	12/2016	141	96
161	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 5,300.00	6,213.84	1,509.46	03/2014 03/2016	12/2016	33	9
162	JIRIBAM TO IMPHAL (TUPU)(NL)(NEFR) - [220100288]NEFR,MANIPUR	04/2003	727.56 727.53	4,478.17	2,023.83	03/2011 03/2014	03/2017	72	36
163	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,TRIPURA	04/2008	813.34 813.34	1,141.75	545.80	03/2014 -	03/2017	36	-
164	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,MIZORAM	04/2008	619.34 -	2,393.48	171.49	04/2014 -	03/2017	35	-
165	SEVOK RANGPO, NEFR - [N22000102]NEFR,SIKKIM	04/2008	1,339.48 -	3,380.58	82.93	12/2015 -	03/2017	15	-
166	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NEFR,NAGALAND	04/2006	850.00 850.00	850.00	9.24	03/2015 -	03/2017	24	-

(March 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
167	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NEFR,ASSAM	04/1996	1,676.31 1,676.31	4,184.84	4,020.98	03/2009 -	03/2017	96	-
168	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NEFR,TRIPURA	04/1999	895.00 -	1,091.98	955.94	03/2007 -	03/2017	120	-
169	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 2,500.00	20,000.00	8,822.50	11/2002 -	12/2017	181	-
170	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]NEFR,ASSAM	09/1997	1,000.00 1,500.00	4,500.00	3,092.23	04/2008 03/2014	12/2017	116	45
171	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NEFR,MULTI STATE	04/2000	733.00 733.00	1,655.81	1,552.32	12/2008 -	03/2018	111	-
172	KATAKHAL TO BHAIKABI - [N22000126]NEFR,ASSAM	04/1998	227.90 227.90	218.36	133.58	12/2012 -	03/2018	63	-
	Total		28,264.29 -	71,904.97	31,468.26				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
173	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	661.58	05/2010 -	03/2014	46	-
174	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	478.00	308.92	10/2013 -	03/2014	5	-
175	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	682.00	307.91	10/2013 -	03/2014	5	-
176	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 331.23	331.23	183.67	07/2009 -	04/2014	57	-
177	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 361.00	361.00	339.45	02/2009 -	05/2014	63	-
178	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 333.83	333.83	73.71	09/2007 -	05/2014	80	-
179	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	39.49	09/2013 -	07/2014	10	-
	Total		2,693.00 -	3,031.06	1,914.73				
	<u>SHIPPING AND PORTS</u>								
180	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 1,460.00	2,158.16	1,004.31	12/2010 09/2012	10/2015	58	37
	Total		1,228.00 -	2,158.16	1,004.31				
	<u>TELECOMMUNICATIONS</u>								
181	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	384.00	29.45	10/2010 03/2012	03/2014	41	24
182	SUPPLY INSTALLATION TESTING AND COMMISSIONING OF RURAL WIMAX NETWORK PHASE-II - [N26000100]BSNL,MULTI STATE	07/2010	1,148.19 -	964.37	249.32	05/2011 -	05/2014	36	-
183	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTANCHAL - [N26000058]BSNL,UTTARAKHAND	01/2009	149.15 -	158.72	84.68	06/2009 -	06/2014	60	-

(March 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
184	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL,ASSAM	06/2007	336.81 -	336.81	183.16	01/2009 -	06/2014	65	-
	Total		2,018.15 -	1,843.90	546.61				
	<u>URBAN DEVELOPMENT</u>								
185	FARIDABAD EXTENSION - [N28000057]DMRC,DELHI	09/2011	2,494.00 -	2,494.00	551.23	09/2014 -	05/2015	8	-
	Total		2,494.00 -	2,494.00	551.23				
	Grand Total		424,016.89	512,494.67	296,343.81				

List of ongoing projects having cost overrun w.r.t. to revised schedule

(March 2014)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	12/2008 -	12/2014	31.12
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	03/2015	62.57
	Total		16,663.00 -	22,947.00			
	<u>CIVIL AVIATION</u>						
3	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]	08/2008	1,942.51 -	2,593.13	05/2011 -	03/2013	33.49
4	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]	05/2010	335.61 -	388.53	05/2012 -	04/2014	15.77
	Total		2,278.12 -	25,928.66			
	<u>COAL</u>						
5	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37
6	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.00 -	490.10	03/2017 -	03/2017	0.02
7	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]	12/2009	321.42 -	321.50	03/2014 -	03/2016	0.02
8	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	03/2016 -	03/2016	31.87
	Total		1,431.79 -	27,645.25			
	<u>PETROCHEMICALS</u>						
9	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	8,920.00	04/2012 -	-	63.35
	Total		5,460.61 -	36,565.25			
	<u>PETROLEUM</u>						
10	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00 -	32,710.00	11/2012 -	12/2014	9.85
11	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I [N16000070]	07/2009	238.68 -	312.00	01/2012 -	07/2013	30.72

(March 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
12	CONSTRUCTION OF SIX EFFLUENT TREATMENT PLANTS (ETP), AHMEDABAD AND ANKLESWAR - [N16000099]	03/2009	234.78 234.78	317.64	09/2012 -	12/2014	35.29
13	WAX PROJECT - [N16000101]	06/2010	576.60 -	676.05	12/2013 -	03/2014	17.25
14	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]	03/2010	3,241.03 -	6,638.94	03/2013 -	11/2014	104.84
15	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]	08/2009	246.81 -	276.83	04/2012 -	06/2014	12.16
16	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	11/2012	309.81 -	309.82	10/2014 -	10/2015	0.00
17	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]	08/2008	144.02 -	204.29	06/2012 -	06/2014	41.85
	Total		34,768.73 -	78,010.82			
	<u>POWER</u>						
18	PARBATI HEP (NHPC) II - [180100210]	09/2002	3,919.59 -	5,366.00	09/2009 -	07/2018	36.90
19	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]	09/2003	6,285.33 -	10,667.00	09/2010 -	07/2018	69.71
20	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	4,653.95	12/2009 06/2016	03/2017	86.39
21	BARH STPP(3X660MW) NTPC - [180100242]	12/2003	8,692.97 -	8,693.00	12/2009 -	03/2017	0.00
22	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]	09/2005	1,061.38 -	1,501.75	09/2009 -	07/2015	41.49
23	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]	03/2005	596.45 -	1,007.16	12/2007 -	-	68.86
24	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]	10/2005	2,304.56 -	2,716.00	10/2010 -	08/2014	17.85
25	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	03/2017	29.14
26	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,745.08	07/2014 -	07/2018	50.31
27	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,128.38	08/2013 -	09/2015	96.59
28	MOUDA STPP - [N18000048]	11/2008	5,459.28 -	6,010.89	08/2012 -	03/2013	10.10
29	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]	08/2008	2,360.95 -	2,580.90	08/2012 -	03/2014	9.32
30	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	951.48	07/2013 -	11/2014	126.00
	Total		39,642.47 -	130,878.71			
	<u>RAILWAYS</u>						

(March 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
31	VIRAMGAM-BHILDI(WR),GC - [220100062	04/1990	155.66 -	548.01	- 03/2010	-	252.06
32	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	925.30	- -	02/2014	643.63
33	AMRAVATI-NARKHER NL(CR) - [220100118	06/1994	120.90 175.30	725.00	06/1999 -	03/2011	499.67
34	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	20,000.00	11/2002 -	12/2017	700.00
35	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135	04/1983	36.80 274.41	703.17	- -	03/2015	1,810.79
36	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	968.60	12/2012 -	-	218.62
37	CALICUT-MANGALORE (DL) (SR) - [220100151	02/1996	240.00 -	579.37	- -	02/2012	141.40
38	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	401.81 -	1,814.10	03/2004 -	12/2014	351.48
39	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181	02/1997	353.08 -	2,820.00	- -	-	698.69
40	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	37.68 -	1,036.78	07/2012 -	-	2,651.54
41	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	800.00	- -	10/2012	414.30
42	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192	03/1996	155.74 164.36	883.00	02/2009 -	03/2012	466.97
43	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	- -	-	840.53
44	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197	03/1997	395.00 598.98	1,708.41	- -	03/2013	332.51
45	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201	09/1997	1,000.00 -	4,500.00	04/2008 12/2011	12/2017	350.00
46	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	645.00	- -	03/2014	195.55
47	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	31.42 154.30	445.40	03/2007 03/2007	03/2015	1,317.57
48	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	596.36	06/2004 -	12/2014	207.29
49	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
50	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	925.00 -	1,630.97	05/2008 -	-	76.32
51	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240	04/1997	233.00 335.77	1,043.56	03/2012 -	-	347.88
52	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	12/2009 -	03/2014	300.67
53	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	100.00 -	725.53	12/2010 -	03/2015	625.53

(March 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
54	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	550.00 -	1,566.00	- -	-	184.73
55	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	832.00	- 05/2009	05/2009	243.21
56	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	409.00 408.76	847.75	06/2007 -	06/2007	107.27
57	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	900.00	- -	-	800.00
58	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) [220100263	03/1998	280.00 -	1,122.00	- -	03/2013	300.71
59	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	1,655.81	12/2008 -	03/2018	125.90
60	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM- NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	907.69 -	3,176.10	12/2006 -	08/2010	249.91
61	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	02/2011 -	03/2013	191.48
62	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	1,423.98	03/2005 12/2008	12/2016	1,172.55
63	JIND-SONEPAT (NL),NR - [220100280	01/2004	190.81 -	740.00	03/2012 -	12/2012	287.82
64	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	355.38 -	1,995.25	- -	12/2014	461.44
65	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06
66	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	288.00	02/2009 02/2009	08/2014	73.33
67	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	4,478.17	03/2011 -	03/2017	515.51
68	KOSI BRIDGE (NL), ECR - [220100304	04/2002	323.41 -	341.41	03/2012 -	03/2013	5.57
69	DANIAWAN-BIHARSARIF (NL), ECR - [220100311	04/2001	104.79 -	406.92	- -	-	288.32
70	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314	04/2001	727.13 727.13	1,225.90	- -	-	68.59
71	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315	01/2004	915.70 -	2,232.50	- -	03/2015	143.80
72	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316	04/2003	218.19 -	472.00	- -	02/2013	116.33
73	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	585.93	- -	12/2013	52.67
74	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	818.29	02/2015 -	02/2015	346.59
75	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	276.00	03/2009 03/2009	08/2014	106.88
76	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329	04/2003	136.62 -	289.93	12/2007 03/2010	-	112.22

(March 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
77	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	114.01 283.95	477.88	03/2012 -	03/2013	319.16
78	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56 -	791.59	- -	-	109.11
79	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 -	1,117.11	03/2008 06/2008	-	50.35
80	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N22000052]	04/2003	98.74 -	337.30	- -	03/2012	241.60
81	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	385.54	03/2010 -	-	18.66
82	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41
83	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY'-AGASTIYAMPALLI - [N22000079]	09/2007	404.19 -	1,383.45	- -	-	242.28
84	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	914.98	- -	12/2012	166.63
85	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	485.00	03/2011 -	03/2011	185.29
86	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR - [N22000083]	09/1996	156.00 -	406.40	- -	03/2014	160.51
87	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 -	420.00	- -	-	236.00
88	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	820.00	- -	-	79.82
89	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	385.20	- -	03/2018	92.60
90	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	300.00 -	532.87	- -	-	77.62
91	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,116.53	03/2010 -	03/2017	243.55
92	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	6,213.84	03/2014 -	12/2016	17.24
93	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	246.44	03/2012 -	03/2014	44.03
94	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,074.45	06/2005 -	06/2016	265.50
95	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	1,141.75	03/2014 -	03/2017	40.38
96	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,393.48	04/2014 -	03/2017	286.46
97	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	359.86	- -	03/2015	27.20
98	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	3,380.58	12/2015 -	03/2017	152.38

(March 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
99	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111	04/2010	2,619.02 -	2,913.51	03/2016 -	03/2016	11.24
100	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113	04/2008	653.19 -	653.47	03/2014 -	03/2014	0.04
101	GHUTIASHARIF-CANNING (ER) - [N22000117	04/2009	189.97 -	611.03	12/2011 -	11/2013	221.65
102	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120	04/2008	603.04 -	1,421.25	03/2012 -	-	135.68
103	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123	04/2008	318.24 -	484.61	03/2012 -	-	52.28
104	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127	04/1996	1,676.31 -	4,184.84	03/2009 -	03/2017	149.65
105	CHHAPRA-BALLIA UP - [N22000134	03/2013	295.00 -	494.92	-	-	67.77
106	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143	04/1994	320.66 -	913.48	-	-	184.87
107	VIRAMGAM-SAMAKHIALI (DL) - [N22000145	04/2011	446.00 -	685.17	-	-	53.63
108	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITSURGARH-UDAIPUR - [N22000152	04/2013	456.00 -	965.16	-	-	111.66
109	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153	04/2010	739.65 -	872.22	-	-	17.92
110	AJMER-BANGURGRAM - [N22000155	04/2011	213.39 -	218.39	-	-	2.34
111	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160	04/2010	553.63 -	651.17	-	-	17.62
112	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162	04/2010	149.90 -	177.38	03/2015 -	12/2015	18.33
113	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163	04/2010	146.95 -	171.02	06/2013 -	06/2014	16.38
114	SAKRI-HASANPUR ROAD (NL) - [N22000171	04/1999	175.69 -	325.00	-	-	84.98
115	CHHAPRA-MUZAFFARPUR (NL) - [N22000172	04/2006	285.07 -	378.56	-	-	32.80
116	ATTIPPATTU-PUTTUR - [N22000184	04/2008	446.87 -	528.00	-	-	18.16
117	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185	04/2008	523.52 -	1,200.00	-	-	129.22
118	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187	04/1999	198.68 -	556.64	-	-	180.17
119	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188	04/1999	271.24 -	520.00	-	-	91.71
120	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189	04/2008	822.39 -	1,280.83	-	-	55.74

(March 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
121	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
122	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	222.21	- -	-	0.36
123	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,091.98	03/2007 -	03/2017	22.01
124	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22	- -	-	109.04
125	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	-	173.71
126	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	247.00 -	951.24	- -	12/2014	285.12
127	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	222.95	- -	-	16.29
128	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]	04/1999	523.17 -	1,327.78	- -	-	153.80
129	HYDERABAD/SECUNDERABD MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II - [N22000213]	04/2012	632.68 -	816.55	04/2012 -	03/2016	29.06
130	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	800.00	- -	-	33.02
131	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	697.00 -	2,501.05	- -	-	258.83
132	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70 -	279.70	- -	-	0.72
133	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	182.06 -	184.06	- -	-	1.10
134	PANVEL PEN DOUBLING - [N22000255]	04/2006	191.00 -	260.16	- -	05/2014	36.21
135	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26
136	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	-	651.97
137	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97
138	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]	04/2008	184.26 -	2,000.00	- -	-	985.42
139	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]	04/2012	289.79 -	377.44	- -	-	30.25
140	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	755.54	- -	-	163.25
141	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99	- -	-	183.41
142	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29
143	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	329.97	- -	-	50.10

(March 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
144	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303	04/1999	460.94 -	1,030.00	01/1999 -	-	123.46
	Total		51,870.80 -	271,549.53			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
145	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221	12/2003	155.00 -	201.66	09/2008 -	-	30.10
146	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236	12/2003	166.27 -	193.10	03/2008 -	-	16.14
147	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279	12/2003	167.64 -	265.63	11/2008 -	12/2014	58.45
148	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	02/2010 -	-	2.29
149	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	-	106.50
	Total		1,871.91 -	274,779.23			
	<u>SHIPPING AND PORTS</u>						
150	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016	11/2007	1,228.00 -	2,158.16	12/2010 -	10/2015	75.75
151	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	06/2014	300.00
152	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA, KANDLA PORT TRUST [N25000037	04/2005	882.00 -	1,060.00	02/2011 -	12/2012	20.18
153	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039	12/2005	702.00 -	755.50	03/2011 -	03/2013	7.62
154	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053	10/2010	966.46 -	994.82	02/2014 -	04/2014	2.93
155	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST [N25000059	03/2007	245.67 -	373.22	04/2009 -	02/2011	51.92
	Total		4,174.13 -	280,720.93			
	<u>STEEL</u>						
156	EXPANSION OF IISCO STEEL PLANT - [N12000051	06/2008	14,443.00 -	16,408.00	12/2011 -	06/2014	13.61
157	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA [N12000079	06/2012	237.09 -	254.90	12/2014 -	12/2014	7.51
158	REBUILDING OF BATTERY BLOCK 5A AND RE- CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080	11/2012	313.05 -	339.35	06/2015 -	06/2015	8.40

(March 2014)

Date of Commissioning							
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	Total		14,993.14 -	297,723.18			
	<u>TELECOMMUNICATIONS</u>						
159	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058]	01/2009	149.15 -	158.72	06/2009 -	06/2014	6.42
160	GSM EQUIPMENT OF 799000 LINES (2G) 101000 LINES (3G) JHARKHAND PHASE V.1 TELECOM CIRCLE - [N26000088]	03/2008	328.13 -	392.13	03/2009 -	01/2013	19.50
161	GSM EQUIPMENT OF 1625000 LINES (2G) 325000 LINES (3G) MP PHASE V.1 TELECOM CIRCLE - [N26000090]	11/2009	916.70 -	930.60	11/2010 -	09/2013	1.52
	Total		1,393.98 -	299,204.63			
	<u>URBAN DEVELOPMENT</u>						
162	BANGALORE METRO RAIL PROJECT - [N28000008]	05/2006	6,395.00 -	11,609.00	06/2011 -	03/2013	81.53
	Total		6,395.00 -	310,813.63			
	<u>WATER RESOURCES</u>						
163	PAGLADIYA DAM PROJECT - [300100001]	01/2001	542.90 -	1,187.00	12/2007 -	12/2012	118.64
	Total		542.90 -	312,000.63			
	Grand Total		181,486.58	2,368,767.45			
