

**353rd FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(Rs.150 crore and above)
March 2015**



PORT TRUST - SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India Ltd.
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead Travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised Catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Operation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petroleum Corporation Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative Ltd.
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation Ltd.
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Corporation.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Corporation.
NCL	Northern Coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation Ltd.
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corporation Ltd.
NGN	Next Generation Network
NLC	Neyveli Lignite Corporation Ltd.
NMDC	National Mineral Development Corporation Ltd.
NPC	Nuclear Power Corporation Ltd.
NRL	Numaligarh Refinery Ltd.
OB	Over Burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over Bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India Ltd.
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

कार्यकारी सारांश

1. मार्च, 2015 की फलैश रिपोर्ट में रु.150 करोड़ और उससे अधिक लागत वाली केन्द्रीय क्षेत्र की 751 अवसंरचनात्मक परियोजनाओं की स्थिति दी गई है। मार्च, 2015 के दौरान 7 परियोजनाओं(पेट्रोलियम तथा विद्युत प्रत्येक क्षेत्र में 3 परियोजनाएं और शहरी विकास क्षेत्र में 1 परियोजना) के पूरा होने की सूचना दी गई है।

2. संदर्भाधीन माह के दौरान, 751 परियोजनाओं में से, 328 परियोजनाओं में मूल समय-सारणी की तुलना में विलंब हुआ तथा 36 परियोजनाओं के संबंध में पिछले माह में सूचित की गई समापन की तारीख की तुलना में अतिरिक्त विलंब की सूचना दी गई है। इन 36 परियोजनाओं में से, 15 परियोजनाएं रु. 1000 करोड़ और अधिक लागत वाली बड़ी परियोजनाएं हैं।

क्र.सं.	क्षेत्र	निगरानी के तहत आने वाली परियोजनाएं (सं.)	मूल समय-सारणी की तुलना में विलंबित परियोजनाएं (सं.)	रिपोर्ट वाले माह के दौरान अतिरिक्त विलंबित परियोजनाएं (सं.)	अतिरिक्त विलंबित बड़ी परियोजनाएं (सं.)
1.	रेलवे	288	35	0	0
2.	सड़क परिवहन एवं राजमार्ग	134	104	5	5
3.	विद्युत	105	63	11	4
4.	पेट्रोलियम	72	43	5	1
5.	कोयला	73	37	4	1
6.	शहरी विकास	30	17	7	1
7.	इस्पात	25	17	1	1
8.	नागर विमानन	7	5	1	0
9.	पोत परिवहन एवं पत्तन	6	0	0	0
10.	परमाणु ऊर्जा	4	4	2	2
11.	दूरसंचार	4	2	0	0
12.	उर्वरक	1	0	0	0
13.	खदान	1	0	0	0
14.	पेट्रो रसायन	1	1	0	0
कुल		751	328	36	15

3. 751 परियोजनाओं के कार्यान्वयन की कुल मूल लागत रु.10,28,235.95 करोड़ थी तथा उनके पूरा होने की अनुमानित लागत रु.12,34,208.57 करोड़ होने की संभावना है, जो रु .2,05,972.62 करोड़ (मूल लागत का 20.03%) की समग्र लागत वृद्धि को दर्शाता है। मार्च, 2015 तक इन परियोजनाओं पर किया गया व्यय रु. 5,44,538.11 करोड़ है, जो परियोजनाओं की अनुमानित लागत का 44.12% है। लागतवृद्धि की अधिकतम प्रतिशतता वाली परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई है:-

लागतवृद्धि की अधिकतम प्रतिशतता वाली (अधिकतम संख्या में पांच) परियोजनाओं की क्षेत्र-वार सूची
(31.03.2015की स्थिति के अनुसार)

क्र.सं.	क्षेत्र/परियोजना_शीर्षक	अनुमोदन की तारीख	मूल लागत (करोड़ रु. में)	अनुमानित लागत(करोड़ रु. में)	लागत वृद्धि(%)
	परमाणु ऊर्जा				
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	13171.00	22462.00	70.54
2	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर (भाविनि, 500 एमडब्ल्यूई)	09/2003	3492.00	5677.00	62.57
	नागर विमानन				
3	नए अंतरराष्ट्रीय टर्मिनल भवन का निर्माण (गोवा)	05/2010	335.61	388.53	15.77
	कोयला				
4	अदरियाला शाफ्ट परियोजना	12/2009	212.34	1228.39	478.50
5	टीपीएस-II विस्तार (1470 मेगावाट से 1970 मेगावाट) (एनएलसी)	10/2004	2030.78	3477.21	71.23
6	मगध ओसी 20 एमटीवाई (सीसीएल)	08/2008	469.78	706.40	50.37
7	तूतीकोरिन ताप विद्युत परियोजना 2X500 मेगावाट	05/2008	4904.54	6602.74	34.63
8	अमलाई ओसी विस्तार, सेक्टर-बी (1.50 एमटीवाई)	11/2009	150.59	198.59	31.87
	पेट्रोरसायन				
9	असम गैस क्रैकर परियोजना	04/2006	5460.61	9834.00	80.09
	पेट्रोलियम				
10	जी1 और जी एस-15 का विकास (ओएनजीसीएल)	04/2003	429.82	3955.21	820.20
11	बी-193 क्लस्टर क्षेत्रों का विकास	06/2007	3248.78	6000.00	84.68
12	विजाग में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	672.00	1178.35	75.35
13	पादुर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	993.00	1693.00	70.49
14	मंगलौर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	732.00	1227.00	67.62
15	कोरबा में मार्केटिंग टीओपी	01/2011	141.86	232.00	63.54
	विद्युत				
16	तुरीअल जल विद्युत परियोजना (60 मेगा.)	07/1998	368.72	1381.71	274.73
17	पारे जल विद्युत परियोजना	12/2008	573.99	1487.49	159.15

18	सुबनसिरी लोअर एच.ई.पी. (8X250 मेगा.) (एनएचपीसी)	09/2003	6285.33	15300.00	143.42
19	त्रिपुरा गैस आधारित विद्युत परियोजना	07/2009	421.01	994.85	136.30
20	पार्वती एचईपी (4X200 मेवा.) (एनएचपीसी) II	09/2002	3919.59	7531.72	92.16
	रेलवे				
21	इकलाखी-बालुरघाट सहित गाजोल-इटाहार से नई बीजी रेलवे लाइन (एनएल), एनईएफआर	04/1983	36.80	1336.57	3531.98
22	बांकुरा-दामोदर (जीसी) (एसईआर)	03/1998	111.90	2371.85	2019.62
23	अकोला-खांडवा जीसी अकोला-अकोट	04/2008	184.26	2000.00	985.42
24	बंगलौर-सत्यमंगलम (एनएल) (एसडब्ल्यूआर)	04/1996	138.00	1382.78	902.01
25	तिरुचिरापल्लई-नागोरे-करायकल्ल (एसआर) (जीसी)	09/1995	100.00	980.00	880.00
	सड़क परिवहन एवं राजमार्ग				
26	पानीपत-जालंधर 6 लेन (96 किमी. से 387.1 किमी.	05/2009	1108.00	2288.00	106.50
27	मैबंग से लुमडिंग (एस-25), 83.400 किमी. से 111.000 किमी.	12/2003	199.81	385.13	92.75
28	मैबंग से लुमडिंग, (एस-24) 111.000 किमी. से 126.450 किमी.	12/2003	155.04	280.13	80.68
29	हरंगाजो से मैबंग, एनएच-54	12/2003	196.00	331.23	68.99
30	ब्रह्मपुत्र ब्रिज एनएच सं.-31	12/2003	217.61	309.56	42.25
	पोत परिवहन एवं पत्तन				
31	एन्नोर मनाली एक्सप्रेस लाइन, एफ/ओ स्पेशल पर्पस व्हीकल (एसपीवी)	10/2002	150.00	600.00	300.00
32	कोचीन पोर्ट ट्रस्ट के वल्लारपदम में आईसीटीटी के लिए रेल सम्पर्क	03/2007	245.67	373.22	51.92
33	2 ऑफशोर कंटेनर बर्थ और टर्मिनल का निर्माण व विकास	11/2007	1228.00	1460.00	18.89
	इस्पात				
34	सिंटर मशीनों - 1 और 2 की सुधार	12/2009	343.00	488.40	42.39
35	3 एमटी से 6.3 एमटी तक तरल इस्पात क्षमता का विस्तार (आरआईएनएल)	10/2005	8692.00	12291.00	41.41
	शहरी विकास				
36	बंगलौर मेट्रो रेल परियोजना	05/2006	6395.00	11609.00	81.53

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीयसलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

4. पूर्ण रूप से लागतवृद्धि की अधिकतम प्रतिशतता वाली (अधिकतम संख्या में पांच)परियोजनाओं की क्षेत्र-वार सूची इस प्रकार हैं:-

अधिकतम लागतवृद्धि वाली (अधिकतम संख्या में 5) परियोजनाओं की क्षेत्र-वार सूची (31.03.2015 की स्थिति के अनुसार)

क्र.सं.	परियोजना शीर्षक	अनुमोदन की तारीख	मूल लागत (रु. करोड़में)	अनुमानित लागत (रु. करोड़ में)	लागतवृद्धि (रु. करोड़ में)
	परमाणु ऊर्जा				
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	13171.00	22462.00	9291.00
2	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर (भाविनि, 500 एमडब्ल्यूई)	09/2003	3492.00	5677.00	2185.00
	नागर विमानन				
3	नई अंतरराष्ट्रीय टर्मिनल भवन का निर्माण (गोवा)	05/2010	335.61	388.53	52.92
	कोयला				
4	तूतीकोरिन ताप विद्युत परियोजना 2X500 मेगावाट	05/2008	4904.54	6602.74	1698.20
5	टीपीएस-II विस्तार (1470 मेगावाट से 1970 मेगावाट) (एनएलसी)	10/2004	2030.78	3477.21	1446.43
6	अदरियाला शाफ्ट परियोजना	12/2009	212.34	1228.39	1016.05
7	मगध ओसी 20 एमटीवाई (सीसीएल)	08/2008	469.78	706.40	236.62
8	अम्लई ओसी विस्तार सेक्टर बी (1.50 एमटीवाई)	11/2009	150.59	198.59	48.00
	पेट्रोरसायन				
9	असम गैस क्रैकर परियोजना	04/2006	5460.61	9834.00	4373.39
	पेट्रोलियम				
10	पारादीप रिफाइनरी परियोजना	02/2009	29777.00	34555.00	4778.00
11	जी1 और जी एस-15 का विकास (ओएनजीसीएल)	04/2003	429.82	3955.21	3525.39
12	बी-193 क्लस्टर क्षेत्रों का विकास	06/2007	3248.78	6000.00	2751.22
13	समेकित रिफाइनरी विस्तार	03/2012	14225.00	16504.00	2279.00

	परियोजना				
	विद्युत				
14	सुबनसिरी लोअर एच.ई.पी. (8X250 मेगावाट) (एनएचपीसी)	09/2003	6285.33	15300.00	9014.67
15	बाढ़ एसटीपीपी (3X660मेगावाट) एनटीपीसी	02/2005	8692.97	15095.67	6402.70
16	पार्वती एचईपी (4X200 मेवा.) (एनएचपीसी) II	09/2002	3919.59	7531.72	3612.13
17	कोल्डम एचईपी (एनटीपीसी)	10/2002	4527.15	7220.00	2692.85
18	बोंगाइगांव थर्मल विद्युत परियोजना	01/2008	4375.35	6749.18	2373.83
	रेलवे				
19	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	03/1995	2500.00	19565.00	17065.00
20	जिरिबाम से इम्फाल (तुपुई)(एनएल)(एनईएफआर)	04/2003	727.56	6570.75	5843.19
21	लुमडिंग-सिलचर जिरिबाम, बदरपुर-बराईग्राम कुमारघाट राष्ट्रीय परियोजना	04/1996	1676.31	5500.00	3823.69
22	बोगीबिल तथा लिंक लाइन पर ब्रह्मपुत्र पुल, एनईएफआर	09/1997	1500.00	4996.19	3496.19
23	सीवोक रंगपो, एनईएफआर	04/2008	1339.48	4190.00	2850.52
	सड़क परिवहन एवं राजमार्ग				
24	पानीपत-जालंधर 6 लेन (96 किमी. से 387.1 किमी.	05/2009	1108.00	2288.00	1180.00
25	मैबंग से लुमडिंग (एएस-25), 83.400 किमी. से 111.000 किमी.	12/2003	199.81	385.13	185.32
26	हरंगाजो से मैबंग, एनएच-54	12/2003	196.00	331.23	135.23
27	मैबंग से लुमडिंग, (एएस-24) 111.000 किमी. से 126.450 किमी. एनएच-54	12/2003	155.04	280.13	125.09
28	आगरा-बाइपास (एनएस-1/यूपी-1), एनएच-2,3	12/2003	348.16	465.50	117.34
	पोत परिवहन एवं पत्तन				
29	एन्नोर मनाली एक्सप्रेस मार्ग, एफ/ओ स्पेशल पर्पज व्हीकल (एसपीवी)	10/2002	150.00	600.00	450.00

30	2 ऑफशोर कंटेनर बर्थ और टर्मिनल का निर्माण और विकास	11/2007	1228.00	1460.00	232.00
31	कोचीन पोर्टट्रस्ट के वल्लारपदम में आसीटीटी के लिए रेल कनेक्टिविटी	03/2007	245.67	373.22	127.55
	इस्पात				
32	तरल इस्पात क्षमता के विस्तार 3 एमटी से 6.3 एमटी तक (आरआईएनएल)	10/2005	8692.00	12291.00	3599.00
33	सिंटर मशीन -1 और 2का सुधार	12/2009	343.00	488.40	145.40
	शहरी विकास				
34	बंगलौर मेट्रो रेल परियोजना	05/2006	6395.00	11609.00	5214.00

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

5. 751 परियोजनाओं में से,3 परियोजनाएं समय से पहले चल रही हैं,123 समय पर तथा 328 परियोजनाएं मूल समय-सारणी की तुलना में विलंबित हैं । तथापि, विलंबित परियोजनाओं की संख्या में 289 तक की कमी हो जाती है यदि विलंब की गणना समापन की अद्यतन समय-सारणी के आधार पर की जाती है । इसके अलावा,33 परियोजनाएं किसी आरंभ संबंधी समय-सारणी/तारीख के बिना स्वीकृत की गई हैं तथा 264 परियोजनाओं के संबंध में न तो शुरू करने का वर्ष और न परियोजना के अनंतिम रूप से पूरा होने की अवधि सूचित की गई है । 328 विलंबित परियोजनाओं में से,72 परियोजनाओं में 1 से 12 माह तक का विलंब हुआ,66 परियोजनाओं में 13 से 24 महीने तक का विलंब हुआ,115 परियोजनाओं में 25 से 60 माह तक का विलंब हुआ तथा 75 परियोजनाओं में 61 माह और उससे अधिक का विलंब हुआ । अधिकतम समयवृद्धि वाली परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई हैं:-

अधिकतम समयवृद्धि वाली (अधिकतम संख्या में 5) परियोजनाओं की क्षेत्र-वार सूची (31.03.2015की स्थिति के अनुसार)

क्र.सं.	क्षेत्र/परियोजना_शीर्षक	अनुमोदन की तारीख	शुरू करने की मूल तारीख	शुरू करने की अनुमानित तारीख	समय वृद्धि (महीना)
	परमाणु ऊर्जा				
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	12/2008	07/2015	79
2	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर (भाविनि, 500 एमडब्ल्यूई)	09/2003	09/2010	09/2016	72
3	काकरापार परमाणु ऊर्जा परियोजना-3 और 4	10/2009	12/2015	10/2017	22

4	राजस्थान परमाणु ऊर्जा परियोजना-7और 8 (2x700 मेवा)	10/2009	12/2016	05/2018	17
	नागर विमानन				
5	सी/ओ पाकयांग (सिक्किम) हवाई अड्डा में नया हवाई अड्डा	01/2009	01/2011	06/2016	65
6	नई अंतरराष्ट्रीय टर्मिनल भवन (गोवा)का निर्माण	05/2010	05/2012	03/2015	34
7	10 हवाई अड्डों में एयरपोर्ट संचालन नियंत्रण केन्द्रों की स्थापना	02/2010	03/2014	04/2015	13
8	विभिन्न हवाई अड्डों में 56 संख्या एयरफील्ड फायर निविदाओं की आपूर्ति	10/2012	03/2015	09/2015	6
9	चंडीगढ़ राष्ट्रीय हवाई अड्डे का विकास (मोहाली) फेज-II	02/2011	03/2015	04/2015	1
	कोयला				
10	कुल्दा ओसीपी (महानदी कोलफील्ड लिमिटेड)	01/2005	03/2010	03/2017	84
11	बलराम ओसीपी विस्तार, एमसीएल 8.00 एमटीवाई	12/2007	03/2010	03/2017	84
12	झंझरा आर-VI सीम पीएसएलडब्ल्यू	11/2006	03/2011	03/2017	72
13	अशोक विस्तार ओसीपी सीसीएल (10 एमटीवाई)	12/2007	03/2011	03/2017	72
14	गोपाल प्रसाद ओसीपी (15 एमटीवीई)	02/2008	03/2015	03/2021	72
	पेट्रोरसायन				
15	असम गैस क्रैकर परियोजना	04/2006	04/2012	06/2015	38
	पेट्रोलियम				
16	जी1 और जी एस-15 का विकास (ओएनजीसीएल)	04/2003	04/2006	06/2015	110
17	जगदीशपुर-हल्दिया पाइपलाइन परियोजना चरण-I	07/2009	01/2013	02/2019	73
18	बी-193 क्लस्टर क्षेत्रों का विकास	06/2007	08/2010	05/2015	57
19	12 ऑफशोर आपूर्ति उपकरणों की निर्माण (ओएसवी)	06/2007	09/2011	12/2015	51
	विद्युत				
20	तुरीअल जल विद्युत परियोजना (60 मेगावाट)	07/1998	07/2006	10/2016	123
21	पार्वती एचईपी (4X200मेगावाट) (एनएचपीसी) II	09/2002	09/2009	12/2018	111
22	बाढ़ एसटीपीपी (3X660 मेगावाट) एनटीपीसी	02/2005	12/2009	03/2018	99

23	कैगा 3 तथा 4 पारेषण प्रणाली (पीजीसीआईएल)	03/2005	12/2007	12/2015	96
24	टेहरी पंज्ड भंडारण संयंत्र (1000 मेगावाट)	07/2006	07/2010	05/2018	94
	रेलवे				
25	गोंडिया-जबलपुर (जीसी), (एसईसीआर)	02/1997	03/1998	12/2019	261
26	गुना-इटावा वाया शिवपुरी-ग्वालियर भिंड एनएल, (एनसीआर)	04/1986	03/1994	03/2015	252
27	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	03/1995	11/2002	12/2018	193
28	बांकुरा-दामोदर (जीसी) (एसईआर)	03/1998	03/2005	12/2019	177
29	तमलुक-दीघा लाइन दोहरीकरण, (एसईआर)	03/1984	06/2005	12/2019	174
	सड़क परिवहन एवं राजमार्ग				
30	असम/पश्चिम बंगाल सीमा से बिजनी चरण-II, 30.00 किमी. से 0.00 किमी., एनएच-31 सी	12/2003	06/2005	12/2015	126
31	हरंगाजो से मैबंग, 164.08 किमी. से 190.587 किमी. एनएच-54	12/2003	09/2007	12/2015	99
32	आगरा-बाइपास (एनएस-1/यूपी-1), एनएच-2,3	12/2003	09/2007	06/2015	93
33	नलवाड़ी से बिजनी (एस-7)	12/2003	04/2008	12/2015	92
34	सिलचर-उदरबंद (चरण. II) एनएच-54, 309 किमी. से 275 किमी.	12/2003	09/2007	03/2015	90
	इस्पात				
35	आरएमएचपी में लौह अयस्क भंडारण की वृद्धि	07/2007	09/2009	06/2015	69
36	3 एमटी से 6.3 एमटी तक तरल इस्पात क्षमता का विस्तार (आरआईएनएल)	10/2005	10/2009	05/2015	67
37	बोकारो इस्पात संयंत्र का विस्तार	05/2010	12/2011	05/2015	41
38	बैलाडिला लौह अयस्क परियोजना डिपोजिट-11बी (एनएमडीसी)	01/2007	12/2011	03/2015	39
39	भिलाई इस्पात संयंत्र का विस्तार	08/2010	03/2013	09/2015	30
	दूरसंचार				
40	असम टेलीकॉम सर्कल, चरण-V.I, 2जीऔर 3जी	06/2007	01/2009	03/2015	74
41	टर्नकी आधार पर बीएसएनएल में ईआरपी कार्यान्वयन	10/2009	10/2010	09/2015	59
	शहरी विकास				

42	सैन्य एमओडी स्टेशन मामुन पंजाब में वैवाहिक भवन का निर्माण	08/2005	08/2007	03/2015	91
43	नागपुर महाराष्ट्र में राष्ट्रीय फायर सेवा कॉलेज का उन्नयन	06/2010	03/2012	04/2015	37
44	आईआईएसईआर कोलकाताके लिए हरिघंटा कल्याणी में शैक्षिक सहित आवासीय परिसर	01/2009	06/2012	06/2015	36
45	प्रगति मैदान से सटे जमीन पर भारतीय उच्चतम न्यायालय के लिए अतिरिक्त परिसर का निर्माण	07/2012	08/2014	06/2017	34
46	संसदीय सौध संसद भवन परिसर नई दिल्ली मेंभवन के विस्तार हेतु निर्माण कार्य	05/2009	05/2013	11/2015	30

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीयसलाहकार और अधिक समयवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

6. अप्रैल, 2014 में इस मंत्रालय के प्रबोधन पर 727 परियोजनाओं में से 235 परियोजनाओं के संबंध में लागतवृद्धि तथा 282 परियोजनाओं के संबंध में समयवृद्धि की सूचना दी गई है; जबकि मार्च,2015 के दौरान 751 परियोजनाओं में से 226 परियोजनाओं के संबंध में लागतवृद्धि तथा 328 परियोजनाओं के संबंध में समयवृद्धि की सूचना दी गई है । अप्रैल, 2014 की तुलना में लागतवृद्धि की सूचना देने वाली परियोजनाओं की संख्या 32% से घटकर 30% हो गई है जबकि समयवृद्धि की सूचना देने वाली परियोजनाओं की संख्या में वृद्धि 39% से 44% हो गई है (अनुबंध 9 (क) तथा 9(ख)) ।

7. विभिन्न अन्य परियोजना कार्यान्वयन एजेंसियों द्वारा यथा सूचित समयवृद्धि के संक्षिप्त कारणों में भूमि अधिग्रहण में विलंब, वन संबंधी अनुमति में विलंब, उपस्करों की आपूर्ति में विलंब, निधि की कमी, भूवैज्ञानिक गतिविधियां, उपस्कर स्थापित करने में समस्या, भूखनन की स्थिति, सिविल कार्यों में धीमी प्रगति, श्रम की कमी, ठेकेदार द्वारा अपर्याप्त संसाधन जुटाना, माओवादी समस्याएं, न्यायालय मामले, संविदात्मक मुद्दे, आरओयू/आरओडब्ल्यू समस्याएं, कानून और व्यवस्था की स्थिति, आदि शामिल हैं ।

8. मंत्रालय के ऑनलाइन कम्प्यूटरीकृत मॉनीटरिंग सिस्टम (ओसीएमएस) में विभिन्न अवसंरचना परियोजनाओं के पीईआरटी चार्टों से तैयार किए गए लक्ष्यों की निगरानी की परिकल्पना की गई है । परियोजना प्राधिकारियों से नियमित रूप से अनुरोध किया गया है कि वे बेहतर निगरानी को सुचारू

बनाने के लिए प्रत्येक परियोजना के संबंध में उपलब्धियों की सूची की प्रविष्टि करें । तथापि, सभी परियोजना एजेंसियां उपलब्धियों की सूची प्रदान नहीं कर रही हैं । बिना लक्ष्यों वाली पहले की परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई हैं:-

बिना लक्ष्यों वाली पहले की परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची (31.03.2015की स्थिति के अनुसार)

क्र. सं.	क्षेत्र/परियोजना के नाम	अनुमोदन की तारीख	मूल लागत	अनुमानित लागत	संचयी व्यय	शुरू करने की मूल तारीख	शुरू करने की अनुमानित तारीख	उपलब्धि
नागर विमानन								
1	वीएस आई हवाईअड्डे, पोर्टब्लेयर में एकीकृत टर्मिनल भवन का निर्माण	10/2013	314.61	314.61	16.59	एन.आर.	एन.आर.	0
2	विभिन्न हवाईअड्डों पर 56 एनओएस एयरफील्ड फायर टैंडर की आपूर्ति	10/2012	217.60	217.60	0.04	03/2015	03/2016	0
3	गगन परियोजना	09/2008	626.00	626.00	499.08	06/2013	06/2013	0
4	नई अंतरराष्ट्रीय टर्मिनल भवन (गोवा) का निर्माण	05/2010	335.61	388.53	285.00	05/2012	11/2014	0
5	चंडीगढ़ अंतरराष्ट्रीय हवाईअड्डा (मोहाली) का विकास चरण-II	02/2011	452.00	452.00	321.56	03/2015	02/2015	0
कोयला								
1	राज महल ओसी विस्तार	09/2009	153.82	153.82	44.47	03/2014	03/2016	0
2	सोनपुर बजारी (सीओएमबी) ओसीपी (8.0 एमटीवाई)	08/2012	1055.05	1055.05	40.13	03/2018	03/2018	0
3	कपूरियायूजी (पीएसएलडब्ल्यू)	08/2011	988.35	988.35	6.84	04/2017	04/2017	0
4	मूनिडीह XV सीम यूजी	08/2011	1230.27	1230.27	1000.00	04/2015	04/2019	0
5	बिजारी ओसीआरसीई (1.50 एमटीवाई)	05/2014	164.49	164.49	22.10	03/2020	03/2020	0
पेट्रोलियम								
1	विजयपुर और पाटा में पेट्रोलसायन परिसर-II	08/2010	8140.00	8140.00	7117.42	02/2014	12/2014	0
2	बीपीसीआर/एचपीसीआर से एलपीजी संयंत्र उद्घाटन के लिए पाइपलाइन	08/2009	246.81	276.83	262.21	08/2012	10/2014	0

3	केन्द्रीय गैस गैद रिंगस्टेशन और ऑफटेक प्वाइंट	08/2008	144.02	204.29	155.22	06/2012	12/2014	0
4	12 ऑफशोर सप्लाई वेसल्स का निर्माण (ओएसवी)	06/2007	736.65	736.65	470.27	09/2011	12/2015	0
5	2000 एचपी ड्रिलिंग रिग के 2 संख्या की खरीद	04/2010	270.00	270.00	एनआर	12/2014	03/2016	0
विद्युत								
1	सुबान सिरीलो अरएच.ई.पी. (एनएचपीसी)	09/2003	6285.33	15300.00	7019.81	09/2010	12/2018	0
2	ईस्ट कोस्ट एनर्जी प्राइवेट लिमिटेड और एनसीसी बिजली परियोजना लिमिटेड एलटीओए जनरेशन से जुड़ी सामान्य प्रणाली	06/2012	1909.24	1909.24	639.63	06/2015	06/2015	0
3	पूर्वी क्षेत्र को सुदृढ़ बनाने की योजना-XII	05/2014	522.29	522.29	एनआर	11/2016	11/2016	0
4	उत्तरी क्षेत्र भाग ख में ट्रांसफार्मर की वृद्धि	03/2014	155.57	155.57	एनआर	03/2016	05/2016	0
5	उत्तरी क्षेत्र में फाइबर ऑप्टिक संचार प्रणाली की स्थापना	03/2012	198.63	198.63	12.80	09/2014	06/2016	0
रेलवे								
1	विरमगम-भिल्डी (डब्ल्यूआर), जीसी	04/1990	155.66	548.01	199.92	एनआर	एनआर	0
2	नामखाना-चंद्रनगर, काकदीप-बुदाखली और चंद्रनाग के लिए लक्ष्मीकांतपुर-नामखाना, इसके बाद एम.एम.	04/1987	406.99	406.99	141.55	एनआर	एनआर	0
3	गुना-इटावावाया शिवपुरी-ग्वालियर-भिंड एनएल, (एनसीआर)	04/1986	158.77	608.02	595.67	03/1994	10/2014	0
4	गजोली-इटाहर (एनएल), एनई एफआर सहित एक लाखी-बलुरघाट से नई बीजी रेलवेलाइन	04/1983	36.80	703.18	255.54	एनआर	एनआर	0
5	हावड़ा-आमता-चंपादंगाएनएल (एसईआर)	04/1974	393.46	445.40	180.72	03/2007	03/2015	0
सड़क परिवहन एवं राजमार्ग								
1	लखनऊ-रायबरेली	07/1999	635.90	635.90	608.30	07/2012	09/2014	0
2	पानीपत-जालंधर 6 लेन (96 किमी. से 387.1 किमी)	05/2009	1108.00	2288.00	3466.00	11/2011	03/2015	0
3	चिल्कालुरीपेट-विजयवाड़ा 6 लेन	05/2009	572.30	572.30	886.90	10/2011	06/2015	0

	(355किमीसेकिमी434.15)							
4	चेन्नई-टाडा (छहलेन)	04/2009	353.37	353.37	446.20	10/2011	12/2014	0
5	दिल्ली / हरियाणा सीमा से रोहतक	04/2007	486.00	486.00	667.10	05/2010	12/2014	0
पोत परिवहन एवं पतन								
1	कांडला में 13 और 14 का गोंबर्थ का निर्माण	12/2005	702.00	755.50	219.00	03/2011	03/2013	0
2	मुम्बई हार्बर चैनल और जेएनपीटी चैनल को चौड़ा करना और मजबूत बनाना	10/2005	800.00	1571.60	9.70	10/2008	एनआर	0
3	एन्नोर मनाली एक्सप्रेस मार्ग, एफ / ओ स्पेशल पर्पज व्हीकल (एसपीवी)	10/2002	150.00	600.00	139.80	03/2006	11/2014	0
4	सेतु समुद्रम शिप चैनल परियोजना	06/2005	2427.40	2427.40	831.23	10/2008	एनआर	0
5	ट्यूना, कांडला पोर्ट ट्रस्ट के नजदीक टेकरा की बर्थिंग और संबंधित सुविधाओं का निर्माण	04/2005	882.00	1060.00	0.93	02/2011	12/2012	0
इस्पात								
1	एनएमडीसीए की कृतइस्पात संयंत्र	01/2010	15525.00	15525.00	5615.00	05/2015	12/2016	0
दूरसंचार								
1	टर्नकीआधारपरबीएसएनएल मेंईआरपीकार्यान्वयन	10/2009	384.00	384.00	48.95	10/2010	03/2015	0
2	असमटेलीकॉमसर्किल, चरण-V.I, 2जीऔर3जी	06/2007	336.81	336.81	195.94	01/2009	12/2014	0
3	उत्तरांचल में 283,000 लाइनों (2 जी) और 75,000 लाइनों (3 जी) का जीएसएम उपकरण	01/2009	149.15	158.72	86.05	06/2009	12/2014	0
शहरी विकास								
1	पाताल गंगारासयानीजिलारायगढ़म हाराष्ट्रमेंसी / ओएनआईएसएम परिसर	12/2012	315.00	315.00	53.96	06/2015	08/2015	0
2	सार्वजनिक ट्रेनिंग (सीएपीटी) भोपाल के लिए सेंट्रल अकादमी का निर्माण	12/2012	188.87	188.87	10.64	12/2014	12/2016	0
3	टीडब्ल्यूआइ सं, प्रयोगशाला सहित अवसंरचना स्कूल के मुख्य भवन का निर्माण	11/2012	238.43	238.43	0.00	02/2015	08/2015	0

4	कमंद में आईआईटी मंडी के लिए चरण 1 उत्तर के अंतर्गत विभिन्न भवन	11/2012	270.83	270.83	15.60	11/2014	10/2015	0
5	आरएसवीवाई पटना के तहत बिहार राज्य में राज्य राजमार्गों का विकास	11/2006	2727.89	2727.89	2637.11	03/2010	10/2014	0

एन.आर.: सूचित नहीं

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीयसलाहकार और उपलब्धियों को अंतिम रूप देने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

9. यह भीपाया गया है कि परियोजना एजेंसियां संशोधित लागत अनुमानों तथा अनेक परियोजनाओं को शुरू करने की समय-सारणी को सूचित नहीं कर रही हैं, जो संकेत देता है कि समय/लागत वृद्धि संबंधी आंकड़े कम बताए गए हैं । बिना संशोधित लागत अनुमान वाली शुरूआती (सबसे पुरानी) परियोजनाओं(अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई हैं:-

संशोधित लागत अनुमानों के बिना पहले की (सबसे पुरानी)परियोजनाओं(अधिकतम संख्या में पांच) की क्षेत्र-वार सूची(31-03-2015 कीस्थिति के अनुसार)

क्र.सं.	क्षेत्र/परियोजना_शीर्षक	अनुमोदन की तारीख	मूल लागत (करोड़ रु. में)	अद्यतनसंशोधित लागत नवीनतम(करोड़ रु. में)	संचयी व्यय (करोड़ रु. में)
	नागर विमानन				
1	सी/ओ पाकयांग (सिक्किम) हवाई अड्डा में नया हवाई अड्डा	01/2009	309.46	0.00	323.48
	कोयला				
1	टीपीएस-II विस्तार (1470 मेगावाट से 1970 मेगावाट) (एनएलसी)	10/2004	2030.78	3027.59	3141.90
	पेट्रोरसायन				
1	असम गैस क्रैकर परियोजना	04/2006	5460.61	0.00	8290.22
	पेट्रोलियम				
1	बी-193 क्लस्टर क्षेत्रों का विकास	06/2007	3248.78	5633.44	5886.42
	विद्युत				

1	बाढ़ एसटीपीपी फेज-II	02/2008	7341.04	0.00	8481.00
2	सुबनसिरी लोअर एच.ई.पी. (8X250 मेगावाट) (एनएचपीसी)	09/2003	6285.33	0.00	7323.23
3	पार्वती एचईपी (4X200मेगावाट) (एनएचपीसी) II	09/2002	3919.59	0.00	4902.92
4	किशनगंगा एचईपी (3x110 मेवा)	01/2009	3642.04	0.00	3864.04
5	कामेंग जल विद्युत परियोजना (नीपको)	12/2004	2496.90	0.00	3615.07
	रेलवे				
1	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	03/1995	2500.00	3000.00	10658.34
2	लुमडिंग-सिलचर-जिरिबम बदरपुर-बराईग्राम-कुमारघाट राष्ट्रीय परियोजना	04/1996	1676.31	0.00	4734.45
3	दमदम-नावपारा और नावपारा- एनएससीपी एयरपोर्ट तक विस्तार के साथ टॉलीगंज- गरिया (एमटीपी)	03/2000	1049.69	3385.14	3536.61
4	बोगीबिल तथा लिंक लाइनों पर ब्रह्मपुत्रा पुल, एनईएफआर	09/1997	1500.00	1000.00	3410.06
5	लिंकड फिंगर्स के साथ रंगिया- मुरकौंगसलेक एनईएफआर	01/2004	915.70	915.70	3198.30
	सड़क परिवहन एवं राजमार्ग				
1	बरेली-सीतापुर एनएच सं.-24	03/2011	1046.00	0.00	4030.00
2	पानीपत-जालंधर छः लेनिंग (96 किमी. से 387.1 किमी.)	05/2009	1108.00	0.00	3466.00
3	नागपुर-बेतुल के चार लेनिंग	02/2011	2498.76	0.00	2786.00
4	सूरत-दहिसर (छः लेन) 263किमी. से 502 किमी.	02/2009	1693.75	0.00	2762.00
5	गुजरात/महाराष्ट्र बॉर्डर सूरत- हजिरापोर्ट सेक्शन	03/2010	1509.10	0.00	2686.00
	पोत परिवहन एवं पत्तन				
1	कोचीन पोर्ट्स के बल्लापाड़म में आईसीटीटी के लिए रेल कनेक्टिविटी	03/2007	245.67	0.00	351.18

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीयसलाहकार औरसंशोधित लागत अनुमानों को अंतिम रूप देने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

शुरू करने की संशोधित तारीख के बिना पहले की परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची इस प्रकार है:-

शुरू करने की संशोधित अनुसूची के बिना पहले की (पुरानी) परियोजनाओं(अधिकतम संख्या में पांच) की क्षेत्र-वार सूची(31.03.2015 की स्थिति के अनुसार)

क्र.सं.	क्षेत्र/परियोजना	अनुमोदन की तारीख	शुरू करने की मूल तारीख	शुरू करने की संशोधित तारीख	शुरू करने की अनुमानित तारीख
नागर विमानन					
1	गगनपरियोजना	09/2008	06/2013	एनआर	06/2013
2	वीएसआई हवाईअड्डे, पोर्ट ब्लेयर में नए एकीकृत टर्मिनल भवन का निर्माण	10/2013	एनआर	एन.आर.	एन.आर.
कोयला					
1	शांतिखानी लॉग वॉल परियोजना-एससीसीएल	10/2006	03/2012	एन.आर.	एन.आर.
2	जल्ला राम शॉफ्ट परियोजना	09/2007	03/2013	एन.आर.	एन.आर.
3	रामा गुंडम ओसी II विस्तार	12/2009	03/2012	एन.आर.	एन.आर.
4	मुराडडीहयूजी टर्न की परियोजना	02/2011	04/2014	एन.आर.	04/2014
5	कृष्णाशिला (एनसीएल) (4 एमटीवाई)	06/2011	03/2013	एन.आर.	03/2014
पेट्रोरसायन					
1	असम गैस क्रैकर परियोजना	04/2006	04/2012	एन.आर.	एन.आर.
पेट्रोलियम					
1	एन्नोर में नई विपणन टर्मिनल	11/2006	एन.आर.	एन.आर.	एन.आर.
2	बीपीसीआर /एचपीसीआर से उरान एलपीजी संयंत्र तक एलपीजी के हस्तांतरण के लिए पाइपलाइन	08/2009	08/2012	एन.आर.	एन.आर.

3	एन्नोर-त्रिची-मदुरै एलपीजी पाइप लाइन	05/2013	एन.आर.	एन.आर.	एन.आर.
	विद्युत				
1	कैगा 3 तथा 4 पारेषण प्रणाली (पीजीसीआईएल)	03/2005	12/2007	12/2009	एन.आर.
2	कुंदन कुलम एपीपी ट्रांसप्रणाली (पीजीसीआईएल)	05/2005	09/2008	एन.आर.	03/2013
3	एसआर -XII की व्यवस्था का सुदृढीकरण	02/2010	06/2012	एन.आर.	एन.आर.
4	आंध्र प्रदेश भाग-ए1 केवैमागिरी क्षेत्र में आईएसजीएस परियोजनाओं से जुड़ी सामान्य प्रणाली	03/2012	06/2014	एन.आर.	एन.आर.
	रेलवे				
1	नांगलडैम-तलवाड़ा (एनएल), एन.आर.	03/1981	07/2012	एन.आर.	एन.आर.
2	गजोली-ईटाहर(एनएल), एनईएफआर सहित एक लाखी-बालुर घाट से नई बीजी रेलवेलाइन	04/1983	एन.आर.	एन.आर.	एन.आर.
3	तामलुकदीघा, लाइन दोहरीकरण (एसईआर)	03/1984	06/2005	07/2011	एन.आर.
4	नाम खाना चंद्रनगर काकद्वीप-बुदाखाली तथा चंद्रनगर के लिए लक्ष्मीकांतपुर-नामखाना, इसके बाद एमएम	04/1987	एन.आर.	एन.आर.	एन.आर.
5	विरमगम-भिल्डी (डब्ल्यूआर), जीसी	04/1990	एन.आर.	03/2010	एन.आर.
	सड़क परिवहन एवं राजमार्ग				
1	लखनऊ-रायबरेली	07/1999	07/2012	एन.आर.	09/2014
2	दीवापुरसे यूपी/बिहारसीमा (एलएमएनएचपी-9) एनएच-28, किमी.402-360.915	12/2003	10/2008	एन.आर.	एन.आर.
3	सिलिगुडी से इस्लामपुर (पश्चिमबंगाल-7)	12/2003	07/2008	एन.आर.	एन.आर.
4	नलबाड़ी से बिजनी (एएस-8)	12/2003	06/2008	एन.आर.	एन.आर.
5	पिंपलगांव-नासिक-गोंडी, एनएच-3 (एनएचडीपीचरणाIII)	03/2005	07/2012	एन.आर.	07/2012

पोत परिवहन एवं पत्तन					
1	ट्यूना, कांडला पोर्ट ट्रस्ट के नजदीक टेकरा की बर्थिंग और संबंधित सुविधाओं का निर्माण	04/2005	02/2011	एन.आर.	12/2012
2	सेतु समुद्रम शिप चैनल परियोजना	06/2005	10/2008	11/2010	एन.आर.
3	मुम्बई हार्बर चैनल और जेएनपीटी चैनल को चौड़ा करना और मजबूत करना	10/2005	10/2008	एन.आर.	एन.आर.
4	पारा दीप बंदरगाह पर चैनल का सुदृढीकरण	12/2005	एन.आर.	01/2009	12/2010
5	कांडला में 13 और 14 का गॉबर्थ का निर्माण	12/2005	03/2011	एन.आर.	03/2013
शहरी विकास					
1	सी/ओ सैन्य रक्षामंत्रालय स्टेशन मामुन पंजाब में वैवाहिक आवासीय	08/2005	08/2007	एन.आर.	एन.आर.
2	बंगलोर मेट्रो रेलपरियोजना	05/2006	06/2011	एन.आर.	03/2013
3	सी/ओ बांद्रा कुर्ला कॉम्प्लेक्स, मुंबई में आईडीबीआई के लिए कार्यालय भवन	11/2006	04/2009	एन.आर.	एन.आर.
4	सी/ओएनआईटी कालीकट केरल के लिए मेगा हॉस्टल।।	01/2010	10/2012	एन.आर.	एन.आर.
5	आईआईटी हॉजखास नई दिल्ली में लेक्चर थिएटर और प्रयोगशाला परिसर	01/2010	07/2012	एन.आर.	07/2012

एन.आर.: सूचित नहीं.

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीयसलाहकार और शुरू करने की संशोधित तारीख को अंतिम रूप देनेके लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

10. अतिरिक्त विलंब का क्षेत्र-वार ब्यौरा निम्नानुसार है:-

- परमाणु ऊर्जा क्षेत्र में, सभी 4 परियोजनाएं विलंबित हैं । माह के दौरान, 2 परियोजनाओं 'कुडनकुलम एपीपी, एनपीसीआईएल' तथा 'राजस्थान परमाणुविद्युत परियोजना-7 और 8 (2X700 मेवा), एनपीसीआईएल' में मेसर्स एटम स्टोरी एक्सपोर्ट (एएसई), रसियन फेडरेशन द्वारा आपूर्ति में हुए विलंब तथा मार्च 2011 में जापान में फुकु सीमा घटनाओं के संदर्भ में एईआरबी द्वारा समीक्षा

किए गए विस्तृत अभिकल्प को ध्यान में रखते हुए उक्त मंजूरी की बाद में प्राप्ति के कारण प्रत्येक में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।

ii) इस्पात क्षेत्र में, 25 परियोजनाओं में से 17 परियोजनाएं विलंबित हैं । माह के दौरान, 1 परियोजना '3 एमटी से 6.3 एमटी तक लिक्विड इस्पात क्षमता का विस्तार, आरआईएनएल' में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

iii) नागर विमानन क्षेत्र में, 7 परियोजनाओं में से 5 परियोजनाएं विलंबित हैं । माह के दौरान 1 परियोजना '10 एयरपोर्टों पर एयरपोर्ट ऑपरेशन्स नियंत्रण केन्द्रों की स्थापना, एएआई' में उपस्करों की आपूर्ति में विलंब के कारण 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।

iv) कोयला क्षेत्र में, 73 परियोजनाओं में से 37 परियोजनाएं विलंबित हैं । माह के दौरान, 4 परियोजनाओं के संबंध में अतिरिक्त विलंब की सूचना प्राप्त हुई है। परियोजना 'टीपीएस-II विस्तार (1470 मेवा से 1970 मेवा), एनएलसी' में जांच स्वीकृति तथा सौंपने में विलंब के कारण 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, परियोजना 'विंड पावर परियोजना, का झुनौरकुलम, तमिलनाडु, एनएलसी' में निजी जमीन के अधिग्रहण में विलंब के कारण 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, परियोजना 'कृष्णशीला (4एमटीवाई), एनएलसी' में वन भूमि के अधिग्रहण में विलंब के कारण 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है तथा परियोजना 'ब्लॉक-बी ओसीपी, (3.5 एमटीवाई), एनएलसी' में 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

v) पेट्रोलियम क्षेत्र में, 72 परियोजनाओं में से 43 परियोजनाएं विलंबित हैं । माह के दौरान 5 परियोजनाओं के संबंध में 1-25 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । परियोजना 'माउंडेड बुलेट परियोजना, सीपीसीएल' और 'विजाग में स्ट्रेटजिक कच्चा तेल भंडारण परियोजना, आईएसपीआरएल' में क्रमशः एचटी पारेषण में व्यवधान तथा निर्माण कार्य में धीमी प्रगति के कारण 1 तथा 8 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, परियोजनाएं 'बी-173 ए क्षेत्र की विकसित तेल वसूली, ओएनजीसी' तथा 'पूर्वी ऑफशोर में शैलो वाटर वेल का विकास, ओएनजीसी' में निर्माण कार्य में धीमी प्रगति तथा पुनः निविदा जारी करने के कारण 11 तथा 25 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, परियोजना 'कोच्चीमें एलपीजी टर्मिनल, आईओसीएल' में 15 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

vi) सड़क परिवहन एवं राजमार्ग क्षेत्र में 134 परियोजनाओं में से 104 परियोजनाएं विलंबित हैं । माह के दौरान, 5 परियोजनाओं के संबंध में 6-16 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। परियोजना 'क्वाजिगुंद-बनिहाल 220.00 किमी. से 188.00 किमी., एनएचएआई' में निधि की कमी तथा संविदात्मक मुद्दे के कारण 11 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'नासरी-छनानी, एनएचएआई' में भूमि अधिग्रहण में विलंब के कारण 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'उड़ीसा-छत्तीसगढ़ बॉर्डर की चार लेनिंग, एनएचएआई', 'दिल्ली-आगरा अनुमोदित लंबाई 180.0 किमी., एनएचएआई' तथा 'वालझापेट-पुनामेली किमी. 106.8 से किमी. 13.8, एनएचएआई' में क्रमशः 6, 12 और 16 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

vi) विद्युत क्षेत्र में, 105 परियोजनाओं में से 63 परियोजनाएं विलंबित हैं । माह के दौरान, 11 परियोजनाओं के संबंध में 2-9 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है । परियोजनाएं 'विन्धुआचल-IV और रिहंद-III जेन. परियोजना, पीजीसीआईएल' और 'उत्तरी क्षेत्र की प्रणाली को सुदृढ़ करने की योजना-XXVI, पीजीसीआईएल' में क्रमशः वन संबंधी अनुमति तथा आरओडब्ल्यू समस्याओं के कारण प्रत्येक में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'पल्लटाना जीबीपीपी और बीपीटीएस के साथ जुड़ी पारेषण प्रणाली, पीजीसीआईएल', 'उड़ीसा-भाग बी में चरण-I जेनरेशन परियोजनाओं के लिए पारेषण प्रणाली, पीजीसीआईएल', 'एसआर ग्रिड में प्रणाली को सुदृढ़ करना XIII, पीजीसीआईएल' और 'एस्सार पावर गुजरात लिमिटेड से कनेक्टिविटी के लिए पारेषण प्रणाली, पीजीसीआईएल' में आरओडब्ल्यू समस्या तथा वन संबंधी अनुमति के कारण प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, परियोजनाएं 'उत्तरी क्षेत्र की प्रणाली को सुदृढ़ करने की योजना-XVI, पीजीसीआईएल', 'झारखंड तथा पश्चिम बंगाल भाग-ए1 में चरण-I जेनरेशन परियोजनाओं के लिए पारेषण प्रणाली, पीजीसीआईएल' तथा 'उत्तरी क्षेत्र की प्रणाली को सुदृढ़ करने की योजना-XXIV, पीजीसीआईएल' में वन संबंधी अनुमति में विलंब तथा जलवायु संबंधी बाधाओं के कारण प्रत्येक में 6 माह के विलंब की सूचना प्राप्त हुई है, परियोजना 'ससानतथा मुंद्रा (यूएमपीपी) के लिए एनआर में प्रणाली का सुदृढ़ीकरण, पीजीसीआईएल' में गंभीर आरओडब्ल्यू समस्या के कारण 9 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, परियोजना 'अगरतला गैस टरबाइन संयंत्र कंबाइन्ड साइकिल एक्सटेंशन परियोजना (51 मेवा), नीपको' में 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

viii) शहरी विकास क्षेत्र में, 30 परियोजनाओं में से 17 परियोजनाएं विलंबित हैं । माह के दौरान, 7 परियोजनाओं के संबंध में 1-23 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । परियोजनाएं 'आईआईएसईआर कोलकाता के लिए हरिनगंटा कल्याणी डब्ल्यूबी में अकादमिक सह आवासीय कैंपस, सीपीडब्ल्यूडी' और 'संसद सौध संसद भवन परिसर नई दिल्ली में एक्सटेंशन भवन का निर्माण, सीपीडब्ल्यूडी' प्रत्येक में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, परियोजनाएं 'आईआईएम के लिए फेज सी/ओ स्थायी कैंपस का पहला चरण, सीपीडब्ल्यूडी' और 'नागपुर-महाराष्ट्र में राष्ट्रीय फायर सर्विसेज कॉलेज का उन्नयन, सीपीडब्ल्यूडी' प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, परियोजनाएं 'दिल्ली एमआरटीएस चरण-III, डीएमआरसीएल', 'प्रगति मैदान से सटे जमीन पर भारतीय उच्चतम न्यायालय के लिए अतिरिक्त परिसर का निर्माण, सीपीडब्ल्यूडी' और 'आईआईटी हौज खास नई दिल्ली में लेक्चर थियेटर और लैब कॉम्प्लेक्स, सीपीडब्ल्यूडी' में क्रमशः 9, 17 और 23 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

11. रेलवे मंत्रालय ने अपने द्वारा कार्यान्वित की जा रही सभी चल रही परियोजनाओं की मासिक स्थिति रिपोर्ट इस मंत्रालय को प्रस्तुत करना बंद कर दिया है । इसलिए उपलब्ध सूचना/आंकड़े का प्रयोग रेलवे क्षेत्र की सभी परियोजनाओं के संबंध में किया गया है ।
12. दिनांक 31.03.2015 की स्थिति के अनुसार, विभिन्न क्षेत्रों में `150 करोड़ तथा अधिक लागत वाली परियोजनाओं के संबंध में स्थिति रिपोर्ट में सूचित की गई है ।
13. इसे सचिव, सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय का अनुमोदन प्राप्त है ।

EXECUTIVE SUMMARY

1. The Flash Report for March 2015 contains information on the status of the 751 Central Sector Infrastructure Projects costing ₹150 crore and above. During March 2015, 7 projects (3 projects each are in Petroleum and Power sector and 1 project in Urban Development sector) have reported completion.

2. During the reference month, out of 751 projects, 328 projects are delayed with respect to original schedule and 36 projects have reported additional delays vis-à-vis the date of completion reported in the previous month. Of these 36 projects, 15 are Mega Projects costing ₹ 1000 crore and above.

S.No.	Sector	Projects on monitor (No.)	Delayed Projects w.r.t original schedule (No.)	Additionally delayed during the month under report (No.)	Additionally delayed Mega Projects (No.)
1	RAILWAYS	288	35	0	0
2	ROAD TRANSPORT AND HIGHWAYS	134	104	5	5
3	POWER	105	63	11	4
4	PETROLEUM	72	43	5	1
5	COAL	73	37	4	1
6	URBAN DEVELOPMENT	30	17	7	1
7	STEEL	25	17	1	1
8	CIVIL AVIATION	7	5	1	0
9	SHIPPING AND PORTS	6	0	0	0
10	ATOMIC ENERGY	4	4	2	2
11	TELECOMMUNICATIONS	4	2	0	0
12	FERTILISERS	1	0	0	0
13	MINES	1	0	0	0
14	PETROCHEMICALS	1	1	0	0
Total		751	328	36	15

3. Total original cost of implementation of the 751 projects was ₹10,28,235.95 crore and their anticipated completion cost is likely to be ₹12,34,208.57 crore, which reflects overall cost overruns of ₹2,05,972.62 crore (20.03% of original cost). The expenditure incurred on these projects till March 2015 is ₹5,44,538.11 crore, which is 44.12% of the anticipated cost of the projects. The

sector-wise list of projects (maximum five in numbers) having maximum percentage of cost overruns is as follows:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Percentage of Cost Overruns (as on 31-03-2015)

SN	SECTOR/PROJECT_TITLE	DOA	COST_ORIGINAL	COST_ANTICIPATED	COR (%)
	ATOMIC ENERGY				
1	KUDANKULAM APP (NPCIL)	12/2001	13171.00	22462.00	70.54
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	5677.00	62.57
	CIVIL AVIATION				
3	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA)	05/2010	335.61	388.53	15.77
	COAL				
4	ADRIYALA SHAFT PROJECT	12/2009	212.34	1228.39	478.50
5	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	10/2004	2030.78	3477.21	71.23
6	MAGADH OC 20 MTY (CCL)	08/2008	469.78	706.40	50.37
7	TUTICORIN THERMAL POWER PROJECT- 2X500 MW	05/2008	4904.54	6602.74	34.63
8	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	11/2009	150.59	198.59	31.87
	PETROCHEMICALS				
9	ASSAM GAS CRACKER PROJECT	04/2006	5460.61	9834.00	80.09
	PETROLEUM				
10	DEV OF G1 AND GS-15 (ONGCL)	04/2003	429.82	3955.21	820.20
11	DEVELOPMENT OF B-193 CLUSTER FIELDS	06/2007	3248.78	6000.00	84.68
12	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG	01/2006	672.00	1178.35	75.35
13	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	70.49
14	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	01/2006	732.00	1227.00	67.62
15	MARKETING TOP AT KORBA	01/2011	141.86	232.00	63.54
	POWER				
16	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	07/1998	368.72	1381.71	274.73
17	PARE HYDRO ELECTRIC PROJECT	12/2008	573.99	1487.49	159.15
18	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	15300.00	143.42
19	TRIPURA GAS BASED POWER PROJECT	07/2009	421.01	994.85	136.30
20	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	7531.72	92.16
	RAILWAYS				
21	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	36.80	1336.57	3531.98
22	BANKURA - DAMODAR (GC) (SER)	03/1998	111.90	2371.85	2019.62
23	AKOLA-KHANDWA GC AKOLA-AKOT	04/2008	184.26	2000.00	985.42
24	BANGLORE - SATYAMANGALAM (NL)(SWR)	04/1996	138.00	1382.78	902.01
25	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	09/1995	100.00	980.00	880.00
	ROAD TRANSPORT AND HIGHWAYS				
26	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	106.50

27	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	385.13	92.75
28	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	155.04	280.13	80.68
29	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	331.23	68.99
30	BRAHMPUTRA BRIDGE, NH NO-31	12/2003	217.61	309.56	42.25
	SHIPPING AND PORTS				
31	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	300.00
32	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	245.67	373.22	51.92
33	CONST. AND DEV. OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL	11/2007	1228.00	1460.00	18.89
	STEEL				
34	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	42.39
35	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	10/2005	8692.00	12291.00	41.41
	URBAN DEVELOPMENT				
36	BANGALORE METRO RAIL PROJECT	05/2006	6395.00	11609.00	81.53

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

4. The sector wise list of projects (maximum five in numbers) having maximum cost overruns in absolute term is as below:-

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Cost Overruns
(as on 31-03-2015)**

SN	PROJECT TITLE	DOA	COST_ORIGINAL	COST_ANTICIPATED	COR (RS.)
	ATOMIC ENERGY				
1	KUDANKULAM APP (NPCIL)	12/2001	13171.00	22462.00	9291.00
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	5677.00	2185.00
	CIVIL AVIATION				
3	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA)	05/2010	335.61	388.53	52.92
	COAL				
4	TUTICORIN THERMAL POWER PROJECT- 2X500 MW	05/2008	4904.54	6602.74	1698.20
5	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	10/2004	2030.78	3477.21	1446.43
6	ADRIYALA SHAFT PROJECT	12/2009	212.34	1228.39	1016.05
7	MAGADH OC 20 MTY (CCL)	08/2008	469.78	706.40	236.62
8	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	11/2009	150.59	198.59	48.00
	PETROCHEMICALS				
9	ASSAM GAS CRACKER PROJECT	04/2006	5460.61	9834.00	4373.39
	PETROLEUM				
10	PARADIP REFINERY PROJECT	02/2009	29777.00	34555.00	4778.00
11	DEV OF G1 AND GS-15 (ONGCL)	04/2003	429.82	3955.21	3525.39
12	DEVELOPMENT OF B-193 CLUSTER FIELDS	06/2007	3248.78	6000.00	2751.22
13	INTEGRATED REFINERY EXPANSION PROJECT	03/2012	14225.00	16504.00	2279.00

	POWER				
14	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	15300.00	9014.67
15	BARH STPP(3X660MW) NTPC	02/2005	8692.97	15095.67	6402.70
16	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	7531.72	3612.13
17	KOLDAM HEP (NTPC)	10/2002	4527.15	7220.00	2692.85
18	BONGAIGAON THERMAL POWER PROJECT	01/2008	4375.35	6749.18	2373.83
	RAILWAYS				
19	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	19565.00	17065.00
20	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	727.56	6570.75	5843.19
21	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	04/1996	1676.31	5500.00	3823.69
22	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR	09/1997	1500.00	4996.19	3496.19
23	SEVOK RANGPO, NEFR	04/2008	1339.48	4190.00	2850.52
	ROAD TRANSPORT AND HIGHWAYS				
24	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	1180.00
25	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	385.13	185.32
26	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	331.23	135.23
27	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	155.04	280.13	125.09
28	AGRA-BYPASS(NS-1/UP-1), NH-2,3	12/2003	348.16	465.50	117.34
	SHIPPING AND PORTS				
29	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	450.00
30	CONST. AND DEV. OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL	11/2007	1228.00	1460.00	232.00
31	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	245.67	373.22	127.55
	STEEL				
32	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	10/2005	8692.00	12291.00	3599.00
33	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	145.40
	URBAN DEVELOPMENT				
34	BANGALORE METRO RAIL PROJECT	05/2006	6395.00	11609.00	5214.00

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

5. Out of the 751 projects, 3 projects are ahead of schedule, 123 are on schedule and 328 are delayed with respect to original schedule. However, the number of delayed projects decreases to 289 if delay is calculated on the basis of latest schedule of completion. Further, 33 projects have been sanctioned without original commissioning schedule date and for 264 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 328 delayed projects, 72 projects have overall delay in the range of 1 to 12 months, 66 projects have delay in the range of 13 to 24 months, 115 projects have delay in the range of 25 to 60 months and 75 projects have delay of 61 months and above. The sector wise list of projects (maximum five in numbers) having maximum time overruns is as below:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Time Overruns

(as on 31-03-2015)

S.NO.	PROJECT_TITLE	DOA	DOC_ORIGINAL	DOC_ANTICIPATED	TOR (Month)
	ATOMIC ENERGY				
1	KUDANKULAM APP (NPCIL)	12/2001	12/2008	07/2015	79
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	09/2010	09/2016	72
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	10/2017	22
4	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016	05/2018	17
	CIVIL AVIATION				
5	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	01/2011	06/2016	65
6	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA)	05/2010	05/2012	03/2015	34
7	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS	02/2010	03/2014	04/2015	13
8	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	03/2015	09/2015	6
9	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II	02/2011	03/2015	04/2015	1
	COAL				
10	KULDA OCP (MAHANADI COALFIELDS LTD)	01/2005	03/2010	03/2017	84
11	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	03/2010	03/2017	84
12	JHANJRA R-VI SEAM PSLW	11/2006	03/2011	03/2017	72
13	ASHOK EXPN OCP CCL (10 MTY)	12/2007	03/2011	03/2017	72
14	GOPAL PRASAD OCP (15MTY)	02/2008	03/2015	03/2021	72
	PETROCHEMICALS				
15	ASSAM GAS CRACKER PROJECT	04/2006	04/2012	06/2015	38
	PETROLEUM				
16	DEV OF G1 AND GS-15 (ONGCL)	04/2003	04/2006	06/2015	110
17	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I	07/2009	01/2013	02/2019	73
18	DEVELOPMENT OF B-193 CLUSTER FIELDS	06/2007	08/2010	05/2015	57
19	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	06/2007	09/2011	12/2015	51

	POWER				
20	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	07/1998	07/2006	10/2016	123
21	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	09/2009	12/2018	111
22	BARH STPP(3X660MW) NTPC	02/2005	12/2009	03/2018	99
23	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL)	03/2005	12/2007	12/2015	96
24	TEHRI PUMPED STORAGE PLANT(1000MW)	07/2006	07/2010	05/2018	94
	RAILWAYS				
25	GONDIA-JABALPUR(GC),(SECR)	02/1997	03/1998	12/2019	261
26	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	04/1986	03/1994	03/2015	252
27	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	11/2002	12/2018	193
28	BANKURA - DAMODAR (GC) (SER)	03/1998	03/2005	12/2019	177
29	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	06/2005	12/2019	174
	ROAD TRANSPORT AND HIGHWAYS				
30	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C	12/2003	06/2005	12/2015	126
31	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54	12/2003	09/2007	12/2015	99
32	AGRA-BYPASS(NS-1/UP-1), NH-2,3	12/2003	09/2007	06/2015	93
33	NALBARI T BIJNI (AS-7)	12/2003	04/2008	12/2015	92
34	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	12/2003	09/2007	03/2015	90
	STEEL				
35	AUGMENTATION OF IRON ORE STORAGE IN RMHP	07/2007	09/2009	06/2015	69
36	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	10/2005	10/2009	05/2015	67
37	EXPANSION OF BOKARO STEEL PLANT	05/2010	12/2011	05/2015	41
38	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC)	01/2007	12/2011	03/2015	39
39	EXPANSION OF BHILAI STEEL PLANT	08/2010	03/2013	09/2015	30
	TELECOMMUNICATIONS				
40	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G	06/2007	01/2009	03/2015	74
41	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS	10/2009	10/2010	09/2015	59
	URBAN DEVELOPMENT				
42	C/O MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB	08/2005	08/2007	03/2015	91
43	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARAstra	06/2010	03/2012	04/2015	37
44	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA	01/2009	06/2012	06/2015	36
45	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	07/2012	08/2014	06/2017	34
46	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI	05/2009	05/2013	11/2015	30

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further time overruns.

6. In April 2014, out of 727 projects on the monitor of this Ministry, 235 projects reported cost overruns and 282 projects reported time overruns; while during March 2015, out of 751 projects, 226 projects reported cost overruns and 328 projects reported time overruns. In comparison to April 2014, number of projects reporting cost overruns has gone down from 32% to 30% whereas projects reporting time overruns have increase from 39% to 44% (Annexure 9 (a) & 9 (b)).

7. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in forest clearance, delay in supply of equipments, fund constraints, geological surprises, problems in equipment erection, geo-mining conditions, slow progress in civil works, shortage of labour, inadequate mobilization by the contractor, maoist problems, court cases, contractual issues, ROU/ROW problems, law and order situation, etc.

8. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones drawn from the PERT Charts of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The sector wise list of earliest projects (maximum five in numbers) without milestones is as below:-

**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Milestones
(as on 31-03-2015)**

[illegible]

1	RAJMAHAL OC EXP.	09/2009	153.82	153.82	44.47	03/2014	03/2016	0
2	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	08/2012	1055.05	1055.05	40.13	03/2018	03/2018	0
3	KAPURIA UG(PSLW)	08/2011	988.35	988.35	6.84	04/2017	04/2017	0
4	MOONIDIH XV SEAM UG	08/2011	1230.27	1230.27	1000.00	04/2015	04/2019	0
5	BIJARI OC RCE (1.50 MTY)	05/2014	164.49	164.49	22.10	03/2020	03/2020	0
PETROLEUM								
1	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA	08/2010	8140.00	8140.00	7117.42	02/2014	12/2014	0
2	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT	08/2009	246.81	276.83	262.21	08/2012	10/2014	0
3	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT	08/2008	144.02	204.29	155.22	06/2012	12/2014	0
4	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	06/2007	736.65	736.65	470.27	09/2011	12/2015	0
5	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG	04/2010	270.00	270.00	NR	12/2014	03/2016	0
POWER								
1	SUBANSIRI LOWER H.E.P (NHPC)	09/2003	6285.33	15300.00	7019.81	09/2010	12/2018	0
2	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION	06/2012	1909.24	1909.24	639.63	06/2015	06/2015	0
3	EASTERN REGION STRENGTHENING SCHEME-XII	05/2014	522.29	522.29	NR	11/2016	11/2016	0
4	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B	03/2014	155.57	155.57	NR	03/2016	05/2016	0
5	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION	03/2012	198.63	198.63	12.80	09/2014	06/2016	0
RAILWAYS								
1	VIRAMGAM-BHILDI(WR),GC	04/1990	155.66	548.01	199.92	NR	NR	0
2	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	04/1987	406.99	406.99	141.55	NR	NR	0
3	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR)	04/1986	158.77	608.02	595.67	03/1994	10/2014	0
4	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	36.80	703.18	255.54	NR	NR	0
5	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	393.46	445.40	180.72	03/2007	03/2015	0

	ROAD TRANSPORT AND HIGHWAYS							
1	LUCKNOW-RAIBAREILI	07/1999	635.90	635.90	608.30	07/2012	09/2014	0
2	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	3466.00	11/2011	03/2015	0
3	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15)	05/2009	572.30	572.30	886.90	10/2011	06/2015	0
4	CHENNAI-TADA(SIX LANE)	04/2009	353.37	353.37	446.20	10/2011	12/2014	0
5	DELHI/ HARYANA BORDER TO ROHTAK	04/2007	486.00	486.00	667.10	05/2010	12/2014	0
	SHIPPING AND PORTS							
1	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA	12/2005	702.00	755.50	219.00	03/2011	03/2013	0
2	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL	10/2005	800.00	1571.60	9.70	10/2008	NR	0
3	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	139.80	03/2006	11/2014	0
4	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	2427.40	2427.40	831.23	10/2008	NR	0
5	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST	04/2005	882.00	1060.00	0.93	02/2011	12/2012	0
	STEEL							
1	NMDC INTEGRATED STEEL PLANT	01/2010	15525.00	15525.00	5615.00	05/2015	12/2016	0
	TELECOMMUNICATIONS							
1	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS	10/2009	384.00	384.00	48.95	10/2010	03/2015	0
2	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G	06/2007	336.81	336.81	195.94	01/2009	12/2014	0
3	GSM EQUIPMENT OF 283000 LINES (2G) AND 75100 LINES (3G) IN UTTANCHAL	01/2009	149.15	158.72	86.05	06/2009	12/2014	0
	URBAN DEVELOPMENT							
1	C/O NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA	12/2012	315.00	315.00	53.96	06/2015	08/2015	0
2	CONSTRUCTION OF CENTRAL ACADEMY FOR PUBLIC TRAINING (CAPT) BHOPAL	12/2012	188.87	188.87	10.64	12/2014	12/2016	0
3	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB	11/2012	238.43	238.43	0.00	02/2015	08/2015	0
4	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR	11/2012	270.83	270.83	15.60	11/2014	10/2015	0

	IIT MANDI AT KAMAND							
5	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA	11/2006	2727.89	2727.89	2637.11	03/2010	10/2014	0

N.R.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up milestones.

9. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The sector wise list of earliest (oldest) projects (maximum five in numbers) without revised cost estimates is as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Cost Estimates (as on 31-03-2015)

S.NO.	SECTOR/ PROJ_TITLE	DOA	COST_ORIGINAL (Rs Crore)	COST_REVISIED _LATEST (Rs Crore)	EXPENDITURE_ CUMM (Rs Crore)
	CIVIL AVIATION				
1	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	309.46	0.00	323.48
	COAL				
1	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	10/2004	2030.78	3027.59	3141.90
	PETROCHEMICALS				
1	ASSAM GAS CRACKER PROJECT	04/2006	5460.61	0.00	8290.22
	PETROLEUM				
1	DEVELOPMENT OF B-193 CLUSTER FIELDS	06/2007	3248.78	5633.44	5886.42
	POWER				
1	BARH STPP STAGE -II	02/2008	7341.04	0.00	8481.00
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	0.00	7323.23
3	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	0.00	4902.92
4	KISHANGANGA HEP (3X110 MW)	01/2009	3642.04	0.00	3864.04
5	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	0.00	3615.07
	RAILWAYS				
1	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	3000.00	10658.34
2	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	04/1996	1676.31	0.00	4734.45
3	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	03/2000	1049.69	3385.14	3536.61

4	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR	09/1997	1500.00	1000.00	3410.06
5	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	01/2004	915.70	915.70	3198.30
	ROAD TRANSPORT AND HIGHWAYS				
1	BAREILY-SITAPUR (NH-24)	03/2011	1046.00	0.00	4030.00
2	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	0.00	3466.00
3	4 LANING OF NAGPUR-BETUL	02/2011	2498.76	0.00	2786.00
4	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	02/2009	1693.75	0.00	2762.00
5	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	03/2010	1509.10	0.00	2686.00
	SHIPPING AND PORTS				
1	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	245.67	0.00	351.18

N.R.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised cost estimates.

The sector wise list of earliest projects (maximum five in numbers) without revised commissioning schedule is as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Commissioning Schedule (as on 31.03.2015)

SN	SECTOR/ PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	REVISED DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
	CIVIL AVIATION				
1	GAGAN PROJECT	09/2008	06/2013	NR	06/2013
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	NR	N.R.	N.R.
	COAL				
1	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	03/2012	N.R.	N.R.
2	JALLARAM SHAFT PROJECT	09/2007	03/2013	N.R.	N.R.
3	RAMAGUNDAM OC-II EXTENSION	12/2009	03/2012	N.R.	N.R.
4	MURAIIDH UG TURN-KEY PROJECT	02/2011	04/2014	N.R.	04/2014
5	KRISHNASHILA (NCL) (4MTY)	06/2011	03/2013	N.R.	03/2014
	PETROCHEMICALS				
1	ASSAM GAS CRACKER PROJECT	04/2006	04/2012	N.R.	N.R.
	PETROLEUM				

1	NEW MARKETING TERMINAL AT ENNORE	11/2006	N.R.	N.R.	N.R.
2	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT	08/2009	08/2012	N.R.	N.R.
3	ENNORE-TRICHY-MADURAI LPG PIPELINE	05/2013	N.R.	N.R.	N.R.
POWER					
1	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL)	03/2005	12/2007	12/2009	N.R.
2	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	05/2005	09/2008	N.R.	03/2013
3	SYSTEM STRENGTHENING -XII OF SR	02/2010	06/2012	N.R.	N.R.
4	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1	03/2012	06/2014	N.R.	N.R.
RAILWAYS					
1	NANGALDAM-TALWARA(NL),NR	03/1981	07/2012	N.R.	N.R.
2	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	N.R.	N.R.	N.R.
3	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	06/2005	07/2011	N.R.
4	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	04/1987	N.R.	N.R.	N.R.
5	VIRAMGAM-BHILDI(WR),GC	04/1990	N.R.	03/2010	N.R.
ROAD TRANSPORT AND HIGHWAYS					
1	LUCKNOW-RAIBAREILI	07/1999	07/2012	N.R.	09/2014
2	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915	12/2003	10/2008	N.R.	N.R.
3	SILIGURI TO ISLAMPUR (WB-7)	12/2003	07/2008	N.R.	N.R.
4	NALBARI TO BIJNI (AS-8)	12/2003	06/2008	N.R.	N.R.
5	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	03/2005	07/2012	N.R.	07/2012
SHIPPING AND PORTS					
1	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST	04/2005	02/2011	N.R.	12/2012
2	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	10/2008	11/2010	N.R.
3	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL	10/2005	10/2008	N.R.	N.R.
4	DEEPENING OF CHANNEL AT PARADIP PORT	12/2005	N.R.	01/2009	12/2010

5	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA	12/2005	03/2011	N.R.	03/2013
URBAN DEVELOPMENT					
1	C/O MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB	08/2005	08/2007	N.R.	N.R.
2	BANGALORE METRO RAIL PROJECT	05/2006	06/2011	N.R.	03/2013
3	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI	11/2006	04/2009	N.R.	N.R.
4	C/O MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	10/2012	N.R.	N.R.
5	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI	01/2010	07/2012	N.R.	07/2012

N.R.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised commissioning schedule.

10.The Sector-wise details of additional delays are as under:-

- i) In the **Atomic Energy**, all 4 projects are delayed. During the month, 2 projects 'Kudankulam APP, NPCIL' and 'Rajasthan Atomic Power Project -7 and 8 (2X700 MW), NPCIL' has reported additional delay of 1 month each due to delay in supplies by M/s Atom Sroy Export (ASE), Russian Federation and late receipt of citing clearance in view of detailed design review by AERB in the context of Fukushima events in Japan in March 2011.
- ii) In the **Steel**, out of 25 projects, 17 projects are delayed. During the month 1 project 'Expansion of Liquid Steel Capacity From 3MT TO 6.3MT, RINL' reported additional delay of 1 month (however, no specific reasons have been reported by the project implementing agencies for the delay in this project).
- iii) In the **Civil Aviation**, out of 7 projects, 5 projects are delayed. During the month 1 project 'Establishment of Airport Operations Control Centres at 10 Airports, AAI' is having additional delay of 1 month due to delay in supply of equipments
- iv) In the **Coal Sector**, out of 73 projects, 37 projects are delayed. During the month, 4 projects have reported additional delay. The project 'TPS-II Expansion (1470 MW to 1970MW), NLC' has reported additional delay of 1 month due to delay in acceptance testing and handover, the project 'Wind Power Project, Kazhuneerkulam, Tamilnadu,

NLC' has reported additional delay of 3 months due to delay in acquisition of private land, the project 'Krishnashila (4MTY) NCL' has reported additional delay of 12 months due to delay in acquisition of forest land and the project 'Block-B OCP, (3.5 MTY) NCL' has reported additional delay of 12 months (however, no specific reasons have been reported by the project implementing agencies for the delay in this project).

- v) In the **Petroleum Sector**, out of 72 projects, 43 projects are delayed. During the month, 5 projects have reported additional delays in the range of 1-25 months. The project 'Mounded Bullet Project, CPCL' and 'Strategic Crude Oil Storage Project at Vizag, ISPR' have reported additional delay of 1 and 8 months due to hindrance in HT transmission and slow construction progress respectively, the projects 'Improved Oil Recovery Of B-173A Field, ONGC', and 'Development of Shallow Water Wells In Eastern Offshore, ONGC' have reported additional of 11 and 25 months due to slow construction progress and retendering, the project 'LPG Terminal at Kochi, IOCL' has reported additional delay of 15 months (however, no specific reasons have been reported by the project implementing agencies for the delay in this project).

- vi) In the **Road Transport and Highways Sector**, out of 134 projects, 104 projects are delayed. During the month, 5 projects have reported additional delays in the range of 6-16 months. The project 'Quazigund-Banihal KM.220.00 to KM.188.00, NHAI' has reported additional delay of 11 months due to fund constraints and contractual issues; ; the project 'Nashri- Chanani, NHAI' has reported additional delay of 12 months due to delay in land acquisition; the projects 'Four Laning of Orissa Chattishgarh Border, NHAI', 'Delhi Agra Approved Length 180.0 KM, NHAI' and 'Walajapet Poonamalee KM 106.8 to KM 13.8, NHAI' have reported additional delays of 6, 12 and 16 months respectively (however, no specific reasons have been reported by the project implementing agency for the delay in these projects).

- vii) In the **Power Sector**, out of 105 projects, 63 projects are delayed. During the month, 11 projects have reported additional delays in the range of 2-9 months. The projects 'Transmission System of Vindhuachal -IV and Rihand -III GEN. Project. PGCIL' and 'Northern Region System Strengthening Scheme-XXVI PGCIL' have reported additional delay of 2 months each due to forest clearance and RoW problem respectively, the projects 'Trans. System Associated With Pallatana GBPP and BPTS, PGCIL', 'Transmission System For Phase-I Generation Projects in Orissa-PART B, PGCIL', 'System Strengthening XIII of SR Grid PGCIL' and 'Transmission System For Connectivity of Essar POWER Gujarat Limited,

PGCIL' have reported additional delay of 3 months each due to RoW problem and forest clearance, the projects 'Northern Region System Strengthening Scheme XVI, PGCIL', 'Transmission System For Phase-1 Generation Projects in Jharkhand and West Bengal-PART-A1, PGCIL' and 'Northern Region System Strengthening Scheme-XXIV, PGCIL' have reported additional delay of 6 months each due to delay in forest clearance and climate constraints, the project 'System Strengthening in NR for Sasan and Mundra (UMPP) PGCIL' has reported additional delay of 9 months due to severe RoW problem, the project 'Agartala Gas Turbine Plant Combined Cycle Extension Project (51 MW) NEEPCO' has reported additional delay of 4 months (however, no specific reasons have been reported by the project implementing agencies for the delay in this project).


- viii)** In the **Urban Development** sector, out of 30 projects, 17 projects are delayed. During the month 7 projects have reported additional delay in the range of 1-23 months. The projects 'Academic cum Residential Campus at Haringhanta Kalyani WB for IISER Kolkata, CPWD' and 'Construction of Extension Building to Parliament House Annexe Parliament House Complex New Delhi, CPWD' have reported additional delay of 1 month each, the projects 'Stage I of Phase C/O Permanent Campus For IIM, CPWD' and 'Upgradation of National Fire Services College at Nagpur Maharashtra, CPWD' have reported additional delay of 3 months each, the projects 'Delhi MRTS Phase-III DMRCL', 'Construction of Additional Complex for the Supreme Court of India at Land Adjoining Pragati Maidan, CPWD' and 'Lecture Theater and Lab Complex at IIT Hauz khas New Delhi, CPWD' have reported additional delay of 9, 17 and 23 months respectively (however, no specific reasons have been reported by the project implementing agencies for the delay in this project)

11. The status as on 31.03.2015 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.
12. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

EXECUTIVE SUMMARY

Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	288	0
2	ROAD TRANSPORT AND HIGHWAYS	134	5
3	POWER	105	11
4	COAL	73	4
5	PETROLEUM	72	5
6	URBAN DEVELOPMENT	30	7
7	STEEL	25	1
8	CIVIL AVIATION	7	1
9	SHIPPING AND PORTS	6	0
10	ATOMIC ENERGY	4	2
11	TELECOMMUNICATIONS	4	0
12	FERTILISERS	1	0
13	MINES	1	0
14	PETROCHEMICALS	1	0
	Total	751	36

Sectoral break up of on- going infrastructure projects.

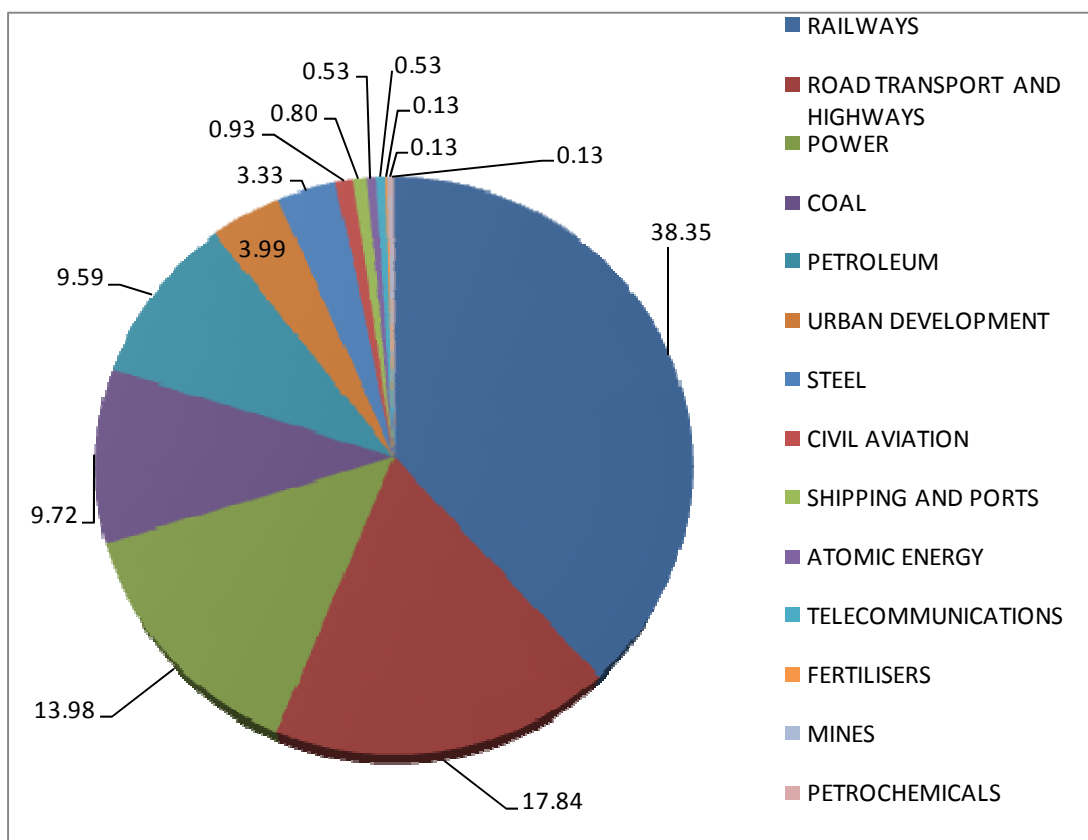

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2014-2015				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	May,2014			
	<u>COAL</u>			
1	BINA EXTN. PROJ(6.0 MTPA) (NORTHERN COAL FIELDS LIMITED) - [N06000019]	168.97	03/2014	67.53
	<u>POWER</u>			
2	PARBATI H.E.P. STAGE -III (NHPC) (NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [180100250]	2,304.56	10/2010	2,349.46
	June,2014			
	<u>PETROLEUM</u>			
3	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000039]	5,713.03	05/2010	3,918.86
4	DEVELOPMENT OF B-46 CLUSTER FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000046]	1,436.21	07/2010	1,165.53
5	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000060]	7,133.39	09/2012	2,795.50
	<u>POWER</u>			
6	MOUDA STPP (NATIONAL THERMAL POWER CORPORATION) - [N18000048]	5,459.28	08/2012	4,056.00
7	VINDHYACHAL STTP STAGE-IV (NATIONAL THERMAL POWER CORPORATION) - [N18000072]	5,915.00	10/2012	3,401.00
8	RIHAND STTP STAGE-III (2X500MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000073]	6,230.81	10/2012	4,357.00
	<u>RAILWAYS</u>			
9	CONSTRUCTION OF NEW LINE FROM HARMATI- ITANAGAR/NARHARIAGUN, NEFR (NORTH EAST FRONTIER RAILWAY) - [N22000083]	156.00	-	424.43
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
10	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106236]	166.27	03/2008	200.40
11	CHITRADURGA-TUMKUR(NH-4) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000157]	839.00	-	692.50
	July,2014			
	<u>STEEL</u>			

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2014-2015

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
12	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREMENT EXP. UNIT (RASTRIYA ISPAT NIGAM LIMITED) - [N12000068]	202.00	01/2010	294.84
13	330 TPH BOILER-6 AND AUXILIARY SYSTEM (RASTRIYA ISPAT NIGAM LIMITED) - [N12000069]	260.00	12/2009	260.75
	<u>PETROLEUM</u>			
14	DEVELOPMENT OF C-SERIES FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000023]	3,195.16	12/2008	3,886.15
15	DEVELOPMENT OF B-22 CLUSTER FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000032]	2,323.40	09/2010	1,916.10
16	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000069]	3,284.00	09/2011	1,916.30
17	ADDITIONAL DEV. OF D-1 FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000086]	2,163.64	06/2012	2,182.31
	<u>POWER</u>			
18	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000106]	425.51	10/2013	386.32
	<u>TELECOMMUNICATIONS</u>			
19	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) PH-5.1 PUNJAB (BHARAT SANCHAR NIGAM LIMITED) - [N26000041]	373.94	12/2008	227.58
20	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK.PROCUREMENT OF GPON EQUIPMANT (BHARAT SANCHAR NIGAM LIMITED) - [N26000072]	952.88	03/2010	20.00
21	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK,PROCUREMENT OF GEAPON EQUIPMENT (BHARAT SANCHAR NIGAM LIMITED) - [N26000073]	152.65	03/2010	29.05
22	GSM EQUIPMENT OF 799000LINES (2G) 101000 LINES 3(G) JHARKHANDPHASE V.1 TELECOM CIRCLE (BHARAT SANCHAR NIGAM LIMITED) - [N26000088]	328.13	03/2009	164.58
23	GSM EQUIPMENT OF 1625000LINES (2G) 325000 LINES 3(G) MP PHASE V.1 TELECOM CIRCLE (BHARAT SANCHAR NIGAM LIMITED) - [N26000090]	916.70	11/2010	828.48
	August,2014			
	<u>PETROLEUM</u>			
24	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I (GAS AUTHORITY OF INDIA LIMITED) - [N16000070]	238.68	01/2012	293.12
25	SINGLE POINT MOORING FACILITY(SMP) PROJECT (MANGALORE REFINERY AND PETROCHEMICALS LIMITED) - [N16000152]	1,043.57	04/2012	648.92
	<u>SHIPPING AND PORTS</u>			
26	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN (PORT TRUST) - [N25000048]	3,500.00	01/2012	3,661.95

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2014-2015

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	September,2014			
	<u>CIVIL AVIATION</u>			
27	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT (AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000037]	1,942.51	05/2011	2,573.92
28	D/O KAMARAJ DOMESTIC TER-PH-II AND EXP. ANNA INT. TER BLDG(K1) (AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000038]	1,808.00	01/2011	1,939.20
	October,2014			
	<u>PETROLEUM</u>			
29	DBNPL SPURLINE (UTTRANCHAL AND PUNJAB) (GAS AUTHORITY OF INDIA LIMITED) - [N16000094]	540.92	06/2011	340.94
30	MRPL PHASE-III EXPANSION (MANGALORE REFINERY AND PETROCHEMICALS LIMITED) - [N16000114]	12,412.00	01/2012	12,205.74
	<u>POWER</u>			
31	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000063]	184.19	11/2011	165.67
32	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATNAM OF ANDHRA PRADESH(PGCIL) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000111]	1,637.34	08/2014	1,499.95
	<u>TELECOMMUNICATIONS</u>			
33	SUPPLY INSTALLATION TESTING AND COMMISSIONING OF RURAL WIMAX NETWORK PHASE-II (BHARAT SANCHAR NIGAM LIMITED) - [N26000100]	1,148.19	05/2011	251.27
	November,2014			
	<u>PETROLEUM</u>			
34	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000138]	246.81	08/2012	263.59
	<u>POWER</u>			
35	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000107]	1,391.97	12/2013	1,472.35
36	TRANSMISSION SYS ASSOCIATED WITH KRISHNAPATNAM UMPP- PART C1 (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000121]	324.33	08/2014	211.36
	<u>SHIPPING AND PORTS</u>			

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2014-2015				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
37	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL (PORT TRUST) - [N25000003]	800.00	10/2008	9.70
38	DEEPENING OF CHANNEL AT PARADIP PORT (PORT TRUST) - [N25000004]	154.84	-	247.89
39	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY VESSELS (SHIPPING CRP. OF INDIA) - [N25000014]	359.44	04/2011	218.00
40	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA, KANDLA PORT TRUST (PORT TRUST) - [N25000037]	882.00	02/2011	1,098.00
41	ACQUISITION OF TWO NOS. OF 3060 DWT (SHIPPING CRP. OF INDIA) - [N25000043]	277.03	12/2011	263.08
42	ACQUISITION OF 4 NOS OF 82000 DWT KAMSAVMAX BULK CARRIERS FROM M/S JIANGSU EASTERN HEAVY INDUSTRIES (SHIPPING CRP. OF INDIA) - [N25000051]	612.72	12/2012	513.36
43	ACQUISITION OF THREE(3) NOS OF 6500TEU CELLULAR CONTAINER VESSELS FROM M/S STX SHIPBUILDING CO. LTD. (SHIPPING CRP. OF INDIA) - [N25000052]	1,028.10	12/2013	554.60
44	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY (SHIPPING CRP. OF INDIA) - [N25000053]	966.46	02/2014	427.54
45	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER (SHIPPING CRP. OF INDIA) - [N25000061]	220.49	01/2013	47.32
46	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY (SHIPPING CRP. OF INDIA) - [N25000062]	511.87	03/2014	106.72
	<u>TELECOMMUNICATIONS</u>			
47	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL (BHARAT SANCHAR NIGAM LIMITED) - [N26000058]	149.15	06/2009	86.34
	December, 2014			
	<u>STEEL</u>			
48	COKE OVEN BATTERY NO. 4 PHASE-II (RASTRIYA ISPAT NIGAM LIMITED) - [N12000038]	108.00	09/2008	168.10
49	EXPANSION OF IISCO STEEL PLANT (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000051]	14,443.00	12/2011	16,640.88
50	EXPANSION OF ROURKELA STEEL PLANT (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000056]	11,812.00	03/2013	11,681.80
	<u>PETROLEUM</u>			
51	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000068]	3,597.00	09/2011	2,299.22
52	POLYPROPYLENE UNIT (MANGALORE REFINERY AND PETROCHEMICALS LIMITED) - [N16000113]	1,803.78	07/2012	995.25
53	GAS TURBINE GENERATION SET (OIL INDIA LIMITED) - [N18000146]	216.88	10/2011	187.14
54	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT (OIL INDIA LIMITED) - [N18000149]	144.02	06/2012	161.88

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2014-2015

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	<u>POWER</u>			
55	RAMPUR HEP(412 MW) (SATLUJ JAL VIDYUT NIGAM LIMITED) - [N18000024]	2,047.03	03/2012	3,350.71
56	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000065]	2,360.95	08/2012	2,150.11
57	765 KV POOLING STATION AND NETWORK WITH DVC AND MAITHOB RBC (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000069]	7,075.33	08/2012	6,413.96
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
58	AMRITSAR-PATHANKOT (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000147]	705.00	11/2012	2,208.00
	<u>SHIPPING AND PORTS</u>			
59	MECHANIZATION OF COAL HANDLING FACILITIES TO 200000 DWT VESSELS ON DBFOT BASIS (PORT TRUST) - [N25000049]	444.10	06/2010	0.01
	January,2015			
	<u>POWER</u>			
60	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000118]	259.28	01/2014	210.02
61	AUGMENTION OF TRANSFORMERS IN NORTHEN REGION - PART A (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000138]	156.04	10/2014	92.86
	<u>RAILWAYS</u>			
62	NEW BG LINE FROM DUDHNOI-MENDIPATAR (NORTH EAST FRONTIER RAILWAY) - [N22000192]	175.43	-	248.12
	February,2015			
63	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU (WORKSHOPS & PRODUCTION UNIT) - [N22000052]	98.74	-	286.19
64	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT (WORKSHOPS & PRODUCTION UNIT) - [N22000053]	470.09	-	1,252.62
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
65	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000226]	1,565.00	10/2014	1,592.00
	March,2015			
	<u>PETROLEUM</u>			

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2014-2015

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
66	WAX PROJECT (NUMALIGARH REFINERY LIMITED) - [N16000101]	576.60	12/2013	606.52
67	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA (GAS AUTHORITY OF INDIA LIMITED) - [N16000112]	8,140.00	02/2014	7,494.38
68	CONSTRUCTION OF 2 FGS IN CHABUA AND BAGHJAN (OIL INDIA LIMITED) - [N18000150]	126.18	06/2012	71.73
	<u>POWER</u>			
69	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000120]	1,310.85	02/2015	1,078.43
70	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000137]	1,935.35	12/2014	1,222.68
71	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000139]	182.80	10/2014	129.93
	<u>URBAN DEVELOPMENT</u>			
72	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000048]	114.18	04/2009	0.01

Month wise List of Deleted Projects Costing Rs. 150 crore and above during				
2014-2015				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	October,2015			
	<u>PETROLEUM</u>			
1	JHAJJAR HISSAR PIPE LINE PROJECT (GAS AUTHORITY OF INDIA LIMITED) - [N06000019]	281.07	10/2010	6.18
	<u>WATER RESOURCES</u>			
2	PAGLADIYA DAM PROJECT (MINISTRY OF WATER RESOURCES) - [180100250]	542.90	12/2007	35.49


Summary of projects in the Flash Report for the month of March, 2015

Project Implementation - Current Status:

Number of Projects in Previous Month	750
Number of Projects completed/dropped/frozen in Current Month	7
Number of Projects elevated to the status of Major project during the current month	3
Number of Projects Added in Current Month	5
Number of Projects in Current Month	751

Brief Analysis


Project Status with respect to Original Schedule: Out of 751 projects, 3 projects are ahead of schedule, 123 projects are on schedule and 328 projects are delayed. Of the balance, 264 projects do not have fixed dates of commissioning while 33 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

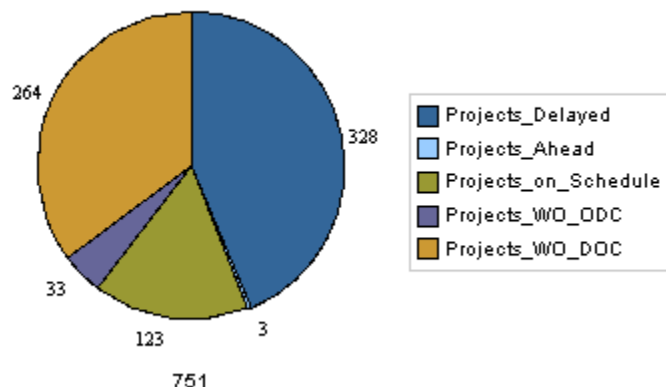

Investment Scenario

Total original cost of implementation of 751 projects when sanctioned, was of the order of Rs. 1028235.95 crore but this was subsequently revised to Rs. 1234208.57 crore implying a cost overrun of 20%. The expenditure incurred on these projects till March, 2015 is Rs. 544538.11 crore, which is 44.1% of the revised cost of the projects.

Figures are in Rs. Crore

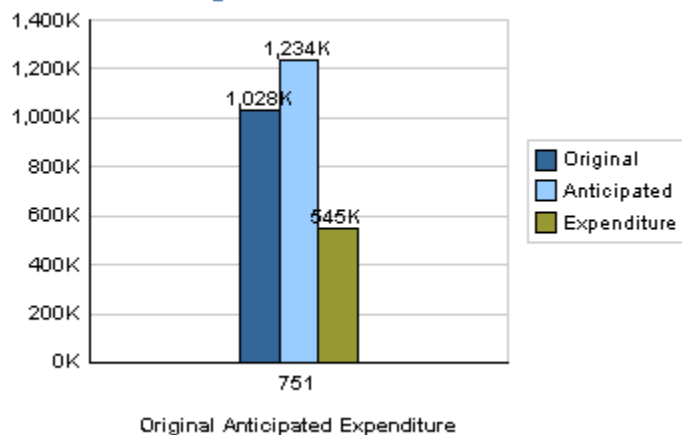

Projects Added / Completed / Dropped / Frozen

No of Projects in Previous Month	750
No of Projects Completed/Dropped/Frozen in Current Month	7
No of Projects added in Current Month	5
No of Projects in Current Month	751

Project status							
Number of Projects							
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total	Delayed Projects (%)
Original (Date)	328	3	123	33	264	751	43.68
Latest Approved (Date)	289	4	161	33	264	751	38.48

Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	639	8,41,683.63	9,25,259.06	3,51,373.87	38.00	83,575.43	9.90
Project with Revision in Cost	112	2,56,829.09	3,08,949.51	1,93,164.24	62.50	52,120.42	20.30
Total	751	10,98,512.72	12,34,208.57	5,44,538.11	44.12	135695.85	12.35
Original Cost of All Projects							
Original Cost	751	10,28,235.95	12,34,208.57	5,44,538.11	44.12	2,05,972.62	20.03

Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	328	575,226.70	699,233.46	421,312.39	60.30	124,006.76	21.60
Latest Approved (RCE)	292	557,275.33	618,648.60	383,359.57	62.00	61,373.27	11.00
Total	620	1,132,502.03	1,317,882.06	804,671.96	61.06	185380.03	16.37

Additional Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	36	104,857.53	119,507.97	69,425.77	58.10	14,650.44	14.00
Total	36	104,857.53	119,507.97	69,425.77	58.09	14650.44	13.97

Extent of cost overrun in projects with respect to original schedule(Sector Wise)									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	2	16,663.00	28,139.00	68.87
2	CIVIL AVIATION	7	2,599.56	2,652.48	2.04	1	335.61	388.53	15.77
3	COAL	73	58,516.59	55,939.62	-4.40	6	8,247.56	12,692.96	53.90
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0.00
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	0.00
6	STEEL	25	59,680.22	63,394.62	6.22	2	9,035.00	12,779.40	41.44
7	PETROCHEMICALS	1	5,460.61	9,834.00	80.09	1	5,460.61	9,834.00	80.09
8	PETROLEUM	72	157,335.33	174,867.00	11.14	19	69,935.40	89,996.02	28.68
9	POWER	105	279,607.51	316,945.69	13.35	23	55,001.54	92,339.72	67.89
10	RAILWAYS	288	163,518.20	289,824.76	77.24	159	82,753.31	209,968.62	153.73
11	ROAD TRANSPORT AND HIGHWAYS	134	100,051.44	101,992.83	1.94	9	2,934.62	4,903.52	67.09
12	SHIPPING AND PORTS	6	5,158.07	5,759.15	11.65	3	1,623.67	2,433.22	49.86
13	TELECOMMUNICATIONS	4	15,131.81	15,131.81	0.00	0	0.00	0.00	0.00
14	URBAN DEVELOPMENT	30	138,680.82	143,894.82	3.76	1	6,395.00	11,609.00	81.53
Total		751	1,028,235.95	1,234,208.57	20.03	226	258,385.32	475,083.99	83.87

Extent of cost overrun in projects with respect to original schedule(State Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overrun			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	27	24,854.07	31,076.50	25.04	7	11,072.36	17,294.79	56.20
2	ARUNACHAL PRADESH	3	9,356.22	21,463.83	129.41	3	9,356.22	21,463.83	129.41
3	ASSAM	36	23,508.04	41,847.73	78.01	15	16,833.87	35,291.22	109.64
4	BIHAR	46	36,458.35	49,774.06	36.52	14	14,265.63	27,801.66	94.89
5	GOA	1	335.61	388.53	15.77	1	335.61	388.53	15.77
6	GUJARAT	29	36,037.34	36,616.51	1.61	4	1,202.26	2,117.22	76.10
7	HARYANA	8	4,259.81	6,230.43	46.26	3	1,633.56	3,604.18	120.63
8	HIMACHAL PRADESH	5	11,681.24	19,906.33	70.41	3	9,493.62	17,718.71	86.64
9	JAMMU AND KASHMIR	7	21,314.62	40,235.30	88.77	2	6,142.04	25,062.72	308.05
10	KARNATAKA	32	64,122.20	79,084.89	23.33	17	13,700.79	28,669.51	109.25
11	KERALA	13	24,457.67	28,611.45	16.98	5	16,205.39	20,359.17	25.63
12	MADHYA PRADESH	20	24,954.32	26,938.24	7.95	4	2,144.95	4,548.31	112.05
13	MAHARASHTRA	46	99,698.94	111,372.81	11.71	12	23,983.77	36,209.67	50.98
14	MANIPUR	1	727.56	6,570.75	803.12	1	727.56	6,570.75	803.12
15	MEGHALAYA	3	4,845.02	6,069.90	25.28	1	4,083.02	5,307.90	30.00
16	MIZORAM	2	988.06	4,201.96	325.27	2	988.06	4,201.96	325.27
17	NAGALAND	2	5,124.00	7,461.12	45.61	2	5,124.00	7,461.12	45.61
18	ODISHA	41	69,075.25	78,163.29	13.16	15	35,919.03	45,028.41	25.36
19	PUNJAB	3	792.50	765.46	-3.41	0	0.00	0.00	0.00
20	RAJASTHAN	25	25,638.72	25,694.20	0.22	7	2,850.42	3,418.90	19.94
21	SIKKIM	2	1,648.94	4,499.46	172.87	1	1,339.48	4,190.00	212.81
22	TAMIL NADU	41	67,950.69	90,688.01	33.46	20	30,028.23	52,765.55	75.72
23	TRIPURA	6	2,966.26	6,617.14	123.08	5	2,678.22	6,363.48	137.60
24	UTTAR PRADESH	28	26,759.70	29,864.04	11.60	9	2,951.38	6,103.98	106.82
25	WEST BENGAL	39	42,838.90	52,229.80	21.92	12	4,495.64	14,409.88	220.53
26	CHANDIGARH	1	452.00	452.00	0.00	0	0.00	0.00	0.00
27	DELHI	11	50,123.12	50,123.12	0.00	0	0.00	0.00	0.00
28	CHHATISGARH	28	80,681.93	75,920.08	-5.90	6	3,494.57	5,157.04	47.57
29	JHARKHAND	33	36,123.28	36,787.95	1.84	6	1,641.96	2,478.40	50.94
30	UTTARAKHAND	6	9,351.89	12,905.21	38.00	4	7,346.89	10,900.21	48.37
31	ANDAMAN & NICOBAR ISLANDS	1	314.61	314.61	0.00	0	0.00	0.00	0.00
32	TELANGANA	21	9,410.62	12,179.13	29.42	5	1,473.01	4,241.83	187.97
33	MULTI STATE	184	211,384.47	239,154.73	13.14	40	26,873.78	55,955.06	108.21
Total		751	1,028,235.95	1,234,208.57	20.03	226	258,385.32	475,083.99	83.87

Extent of time overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	4	40,442.00	51,918.00	17 - 79
2	CIVIL AVIATION	7	2,599.56	2,652.48	2.04	5	1,658.95	1,711.87	1 - 65
3	COAL	73	58,516.59	55,939.62	-4.40	37	28,301.52	32,309.68	8 - 84
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	-
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	-
6	STEEL	25	59,680.22	63,394.62	6.22	17	56,370.71	59,939.71	8 - 69
7	PETROCHEMICALS	1	5,460.61	9,834.00	80.09	1	5,460.61	9,834.00	38 - 38
8	PETROLEUM	72	157,335.33	174,867.00	11.14	43	88,533.32	101,635.31	3 - 110
9	POWER	105	279,607.51	316,945.69	13.35	63	164,942.11	193,265.62	1 - 123
10	RAILWAYS	288	163,518.20	289,824.76	77.24	35	29,092.11	86,252.51	3 - 261
11	ROAD TRANSPORT AND HIGHWAYS	134	100,051.44	101,992.83	1.94	104	77,042.07	78,983.46	5 - 126
12	SHIPPING AND PORTS	6	5,158.07	5,759.15	11.65	0	0.00	0.00	-
13	TELECOMMUNICATIONS	4	15,131.81	15,131.81	0.00	2	720.81	720.81	59 - 74
14	URBAN DEVELOPMENT	30	138,680.82	143,894.82	3.76	17	82,662.49	82,662.49	2 - 91
Total		751	1,028,235.95	1,234,208.57	20.03	328	575,226.70	699,233.46	

Extent of time overrun in projects with respect to original schedule(State Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	27	24,854.07	31,076.50	25.04	10	15,741.93	20,574.54	8 - 73
2	ARUNACHAL PRADESH	3	9,356.22	21,463.83	129.41	2	3,070.89	6,163.83	31 - 87
3	ASSAM	36	23,508.04	41,847.73	78.01	29	21,241.63	36,256.26	11 - 126
4	BIHAR	46	36,458.35	49,774.06	36.52	13	22,113.50	32,170.53	8 - 99
5	GOA	1	335.61	388.53	15.77	1	335.61	388.53	34 - 34
6	GUJARAT	29	36,037.34	36,616.51	1.61	10	24,354.18	24,277.49	6 - 48
7	HARYANA	8	4,259.81	6,230.43	46.26	3	2,244.00	3,424.00	19 - 61
8	HIMACHAL PRADESH	5	11,681.24	19,906.33	70.41	3	8,717.57	15,022.55	11 - 111
9	JAMMU AND KASHMIR	7	21,314.62	40,235.30	88.77	6	13,202.50	32,123.18	10 - 193
10	KARNATAKA	32	64,122.20	79,084.89	23.33	8	19,882.90	20,942.47	2 - 96
11	KERALA	13	24,457.67	28,611.45	16.98	4	2,899.06	3,599.06	15 - 45
12	MADHYA PRADESH	20	24,954.32	26,938.24	7.95	8	3,804.29	3,706.15	12 - 69
13	MAHARASHTRA	46	99,698.94	111,372.81	11.71	23	68,363.53	75,779.48	2 - 144
14	MANIPUR	1	727.56	6,570.75	803.12	1	727.56	6,570.75	96 - 96
15	MEGHALAYA	3	4,845.02	6,069.90	25.28	1	536.00	536.00	14 - 14
16	MIZORAM	2	988.06	4,201.96	325.27	2	988.06	4,201.96	47 - 123
17	NAGALAND	2	5,124.00	7,461.12	45.61	1	850.00	2,973.42	60 - 60
18	ODISHA	41	69,075.25	78,163.29	13.16	19	41,504.00	46,635.71	6 - 84
19	PUNJAB	3	792.50	765.46	-3.41	1	191.24	191.24	91 - 91
20	RAJASTHAN	25	25,638.72	25,694.20	0.22	10	19,145.38	18,699.10	6 - 84
21	SIKKIM	2	1,648.94	4,499.46	172.87	2	1,648.94	4,499.46	51 - 65
22	TAMIL NADU	41	67,950.69	90,688.01	33.46	20	56,193.64	71,194.05	3 - 90
23	TRIPURA	6	2,966.26	6,617.14	123.08	5	2,714.26	5,730.49	5 - 108
24	UTTAR PRADESH	28	26,759.70	29,864.04	11.60	14	9,749.59	11,656.27	5 - 93
25	WEST BENGAL	39	42,838.90	52,229.80	21.92	15	17,678.84	22,344.30	3 - 177
26	CHANDIGARH	1	452.00	452.00	0.00	1	452.00	452.00	1 - 1
27	DELHI	11	50,123.12	50,123.12	0.00	5	42,630.16	42,630.16	8 - 34
28	CHHATISGARH	28	80,681.93	75,920.08	-5.90	15	56,292.51	56,774.57	6 - 39
29	JHARKHAND	33	36,123.28	36,787.95	1.84	16	10,850.42	11,371.50	2 - 138
30	UTTARAKHAND	6	9,351.89	12,905.21	38.00	4	7,605.06	11,048.24	26 - 94
31	ANDAMAN & NICOBAR ISLANDS	1	314.61	314.61	0.00	0	0.00	0.00	-
32	TELANGANA	21	9,410.62	12,179.13	29.42	9	3,370.50	4,570.42	8 - 51
33	MULTI STATE	184	211,384.47	239,154.73	13.14	67	96,126.95	102,725.75	1 - 261
Total		751	1,028,235.95	1,234,208.57	20.03	328	575,226.70	699,233.46	

Extent of time overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	3	36,950.00	46,241.00	17 - 79
2	CIVIL AVIATION	7	2,599.56	2,652.48	2.04	5	1,658.95	1,711.87	1 - 65
3	COAL	73	58,516.59	55,939.62	-4.40	36	22,394.41	26,402.57	8 - 84
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	-
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	-
6	STEEL	25	59,680.22	63,394.62	6.22	16	40,845.71	44,414.71	8 - 69
7	PETROCHEMICALS	1	5,460.61	9,834.00	80.09	1	5,460.61	9,834.00	38 - 38
8	PETROLEUM	72	157,335.33	174,867.00	11.14	22	61,509.21	70,771.05	3 - 73
9	POWER	105	279,607.51	316,945.69	13.35	56	152,744.08	176,411.87	1 - 123
10	RAILWAYS	288	163,518.20	289,824.76	77.24	32	22,617.11	74,893.26	3 - 261
11	ROAD TRANSPORT AND HIGHWAYS	134	100,051.44	101,992.83	1.94	99	76,018.50	77,867.94	5 - 126
12	SHIPPING AND PORTS	6	5,158.07	5,759.15	11.65	0	0.00	0.00	-
13	TELECOMMUNICATIONS	4	15,131.81	15,131.81	0.00	2	720.81	720.81	59 - 74
14	URBAN DEVELOPMENT	30	138,680.82	143,894.82	3.76	17	82,662.49	82,662.49	2 - 91
Total		751	1,028,235.95	1,234,208.57	20.03	289	503,581.88	611,931.57	

Extent of cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overruns			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	51,918.00	51,918.00	0.00	0	0.00	0.00	0.00
2	CIVIL AVIATION	7	2,636.56	2,652.48	0.60	1	335.61	388.53	15.77
3	COAL	73	62,097.62	55,939.62	-9.92	4	4,127.49	4,861.83	17.79
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0.00
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	0.00
6	STEEL	25	63,279.22	63,394.62	0.18	1	343.00	488.40	42.39
7	PETROCHEMICALS	1	8,920.00	9,834.00	10.25	1	8,920.00	9,834.00	10.25
8	PETROLEUM	72	172,377.56	174,867.00	1.44	7	21,257.87	24,131.61	13.52
9	POWER	105	299,768.10	316,945.69	5.73	6	17,820.93	34,998.52	96.39
10	RAILWAYS	288	176,325.78	289,824.76	64.37	153	87,505.12	202,128.68	130.99
11	ROAD TRANSPORT AND HIGHWAYS	134	100,165.39	101,992.83	1.82	8	2,717.01	4,593.96	69.08
12	SHIPPING AND PORTS	6	5,158.07	5,759.15	11.65	3	1,623.67	2,433.22	49.86
13	TELECOMMUNICATIONS	4	15,131.81	15,131.81	0.00	0	0.00	0.00	0.00
14	URBAN DEVELOPMENT	30	138,680.82	143,894.82	3.76	1	6,395.00	11,609.00	81.53
Total		751	1,098,512.72	1,234,208.57	12.35	185	151,045.70	295,467.75	95.61

Extent of time & cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	2	16,663.00	28,139.00	72- 79
2	CIVIL AVIATION	7	2,599.56	2,652.48	2.04	0	0.00	0.00	0- 0
3	COAL	73	58,516.59	55,939.62	-4.40	2	6,935.32	10,079.95	37- 70
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0- 0
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	0- 0
6	STEEL	25	59,680.22	63,394.62	6.22	1	8,692.00	12,291.00	67- 67
7	PETROCHEMICALS	1	5,460.61	9,834.00	80.09	1	5,460.61	9,834.00	38- 38
8	PETROLEUM	72	157,335.33	174,867.00	11.14	9	45,425.86	60,935.53	11- 110
9	POWER	105	279,607.51	316,945.69	13.35	11	22,682.12	35,445.79	8- 123
10	RAILWAYS	288	163,518.20	289,824.76	77.24	5	5,984.97	11,326.25	48- 177
11	ROAD TRANSPORT AND HIGHWAYS	134	100,051.44	101,992.83	1.94	2	425.61	517.56	69- 92
12	SHIPPING AND PORTS	6	5,158.07	5,759.15	11.65	0	0.00	0.00	0- 0
13	TELECOMMUNICATIONS	4	15,131.81	15,131.81	0.00	0	0.00	0.00	0- 0
14	URBAN DEVELOPMENT	30	138,680.82	143,894.82	3.76	0	0.00	0.00	0- 0
Total		751	1028235.95	1234208.57	20.03	33	112269.49	168569.08	

Extent of time & cost overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	2	16,663.00	28,139.00	72- 79
2	CIVIL AVIATION	7	2,599.56	2,652.48	2.04	1	335.61	388.53	34- 34
3	COAL	73	58,516.59	55,939.62	-4.40	5	8,096.97	12,494.37	30- 70
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0- 0
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	0- 0
6	STEEL	25	59,680.22	63,394.62	6.22	1	8,692.00	12,291.00	67- 67
7	PETROCHEMICALS	1	5,460.61	9,834.00	80.09	1	5,460.61	9,834.00	38- 38
8	PETROLEUM	72	157,335.33	174,867.00	11.14	11	43,272.46	58,394.94	11- 110
9	POWER	105	279,607.51	316,945.69	13.35	22	48,716.21	77,039.72	5- 123
10	RAILWAYS	288	163,518.20	289,824.76	77.24	31	23,474.35	80,863.57	3- 261
11	ROAD TRANSPORT AND HIGHWAYS	134	100,051.44	101,992.83	1.94	9	2,934.62	4,903.52	48- 93
12	SHIPPING AND PORTS	6	5,158.07	5,759.15	11.65	0	0.00	0.00	0- 0
13	TELECOMMUNICATIONS	4	15,131.81	15,131.81	0.00	0	0.00	0.00	0- 0
14	URBAN DEVELOPMENT	30	138,680.82	143,894.82	3.76	0	0.00	0.00	0- 0
Total		751	1028235.95	1234208.57	20.03	83	157645.83	284348.65	

List of projects completed/dropped/Frozen during current month							(All Cost /Expenditure in Rs. crore)
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>PETROLEUM</u>						
1	WAX PROJECT	06/2010	576.60	12/2013	676.05	03/2015	606.52
2	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA	08/2010	8,140.00	02/2014	8,752.00	12/2014	7,494.38
3	CONSTRUCTION OF 2 FGS IN CHABUA AND BAGHJAN	08/2008	126.18	06/2012	159.54	03/2015	71.73
	<u>POWER</u>						
4	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH	02/2012	1,310.85	02/2015	1,310.85	03/2015	1,078.43
5	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID	08/2012	1,935.35	12/2014	1,935.35	03/2015	1,222.68
6	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1	01/2013	182.80	10/2014	182.80	03/2015	129.93
	<u>URBAN DEVELOPMENT</u>						
7	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI	11/2006	114.18	04/2009	173.08	N.A.	.01

List of projects added					(All Cost in Rs. crore)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>POWER</u>					
1	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	3/2015	197.40	4/2018	197.40	4/2018
2	INSTALLATION OF STATCOMS IN WESTERN REGION	3/2015	1,071.24	10/2017	1,071.24	10/2017
3	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION	3/2015	550.06	4/2018	550.06	4/2018
4	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	3/2015	1,394.52	6/2017	1,394.52	6/2017
	<u>STEEL</u>					
5	ALTERNATE GAS NETWORK AT BSL	3/2015	255.19	3/2018	255.19	3/2018

Milestones (Cumulative due & achieved)

Total	3724
Achieved up to month	1479


List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>ATOMIC ENERGY</u>						
1	KUDANKULAM APP (NPCIL) NPCIL	13,171.00	22,462.00	12/2008	06/2015	07/2015	1
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) NPCIL	12,320.00	12,320.00	12/2016	04/2018	05/2018	1
	<u>CIVIL AVIATION</u>						
3	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS AAI	344.28	344.28	03/2014	03/2015	04/2015	1
	<u>COAL</u>						
4	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) NLC	2,030.78	3,477.21	06/2009	03/2015	04/2015	1
5	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU NLC	364.75	364.75	10/2014	03/2015	06/2015	3
6	KRISHNASHILA (NCL) (4MTY) NCL	789.88	741.62	03/2013	03/2015	03/2016	12
7	BLOCK-B OCP NCL (3.5 MTY) NCL	746.04	535.10	03/2015	03/2015	03/2016	12
	<u>STEEL</u>						
8	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) RINL	8,692.00	12,291.00	10/2009	04/2015	05/2015	1
	<u>PETROLEUM</u>						
9	MOUNDED BULLET PROJECT AT CPCL CPCL	279.00	279.00	12/2014	06/2015	07/2015	1
10	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG ISPRL	672.00	1,178.35	10/2011	02/2015	10/2015	8
11	IMPROVED OIL RECOVERY OF B-173A FIELD ONGC	352.49	352.49	03/2014	04/2015	03/2016	11
12	LPG TERMINAL AT KOCHI IOCL	607.06	607.06	01/2016	01/2016	04/2017	15
13	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE ONGC	284.82	284.82	04/2015	04/2015	05/2017	25
	<u>POWER</u>						

List of projects reporting additional delays


Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
14	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. PGCIL	4,672.99	4,672.99	11/2012	05/2015	07/2015	2
15	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI PGCIL	803.34	803.34	03/2015	03/2015	05/2015	2
16	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. PGCIL	2,144.00	2,144.00	12/2012	12/2015	03/2016	3
17	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B PGCIL	2,743.19	2,743.19	12/2013	06/2015	09/2015	3
18	SYSTEM STRENGTHENING XIII OF SR GRID PGCIL	487.49	487.49	06/2014	06/2015	09/2015	3
19	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED PGCIL	552.44	552.44	02/2014	06/2015	09/2015	3
20	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) NEEPCO	296.87	363.73	12/2014	01/2015	05/2015	4
21	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI PGCIL	752.64	752.64	07/2013	06/2015	12/2015	6
22	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 PGCIL	558.26	558.26	11/2013	06/2015	12/2015	6
23	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV PGCIL	723.63	723.63	11/2014	06/2015	12/2015	6
24	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) PGCIL	1,216.83	1,216.83	08/2012	06/2015	03/2016	9
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
25	FOUR LANING OF ORISSA CHATTISHGARH BORDER NHAI	1,232.00	1,232.00	08/2015	08/2015	02/2016	6
26	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 NHAI	1,987.00	1,987.00	07/2015	07/2015	06/2016	11
27	NASHRI- CHANANI NHAI	2,159.00	2,159.00	06/2015	06/2015	06/2016	12
28	DELHI AGRA APPROVED LENGTH 180.0 KM NHAI	1,928.22	1,928.22	04/2015	04/2015	04/2016	12
29	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 NHAI	1,287.95	1,287.95	11/2015	11/2015	03/2017	16
	<u>URBAN DEVELOPMENT</u>						

List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
30	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA CPWD	225.81	225.81	06/2012	05/2015	06/2015	1
31	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI CPWD	261.85	261.85	05/2013	10/2015	11/2015	1
32	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM CPWD	332.72	332.72	09/2016	09/2016	12/2016	3
33	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA CPWD	205.00	205.00	03/2012	01/2015	04/2015	3
34	DELHI MRTS PHASE-III DMRCL	38,585.00	38,585.00	03/2016	03/2016	12/2016	9
35	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN CPWD	884.30	884.30	08/2014	01/2016	06/2017	17
36	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI CPWD	162.90	162.90	07/2012	07/2012	06/2014	23

Graphical Presentation of All Projects w.r.t. Original Schedule

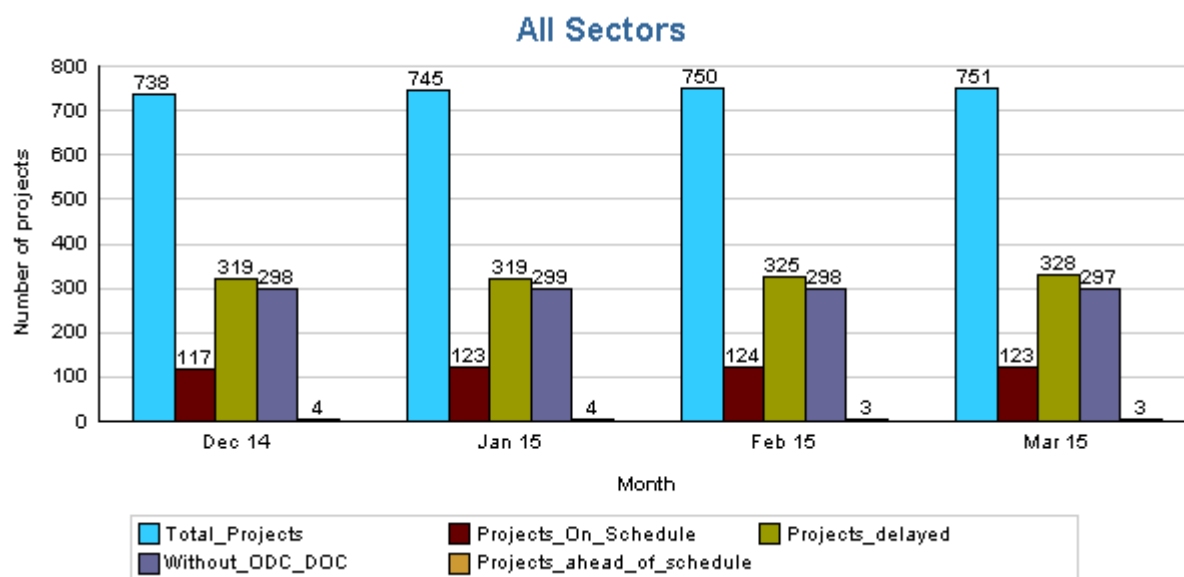

Break-up of 328 Delayed projects in March 2015

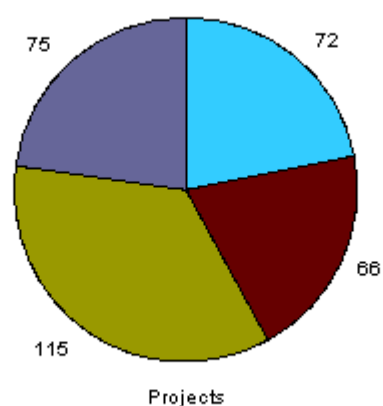


Delay in Months


Legend:

- 1-12
- 13-24
- 25-60
- MORE THAN 60

Graphical Presentation of All Projects w.r.t. Revised Schedule

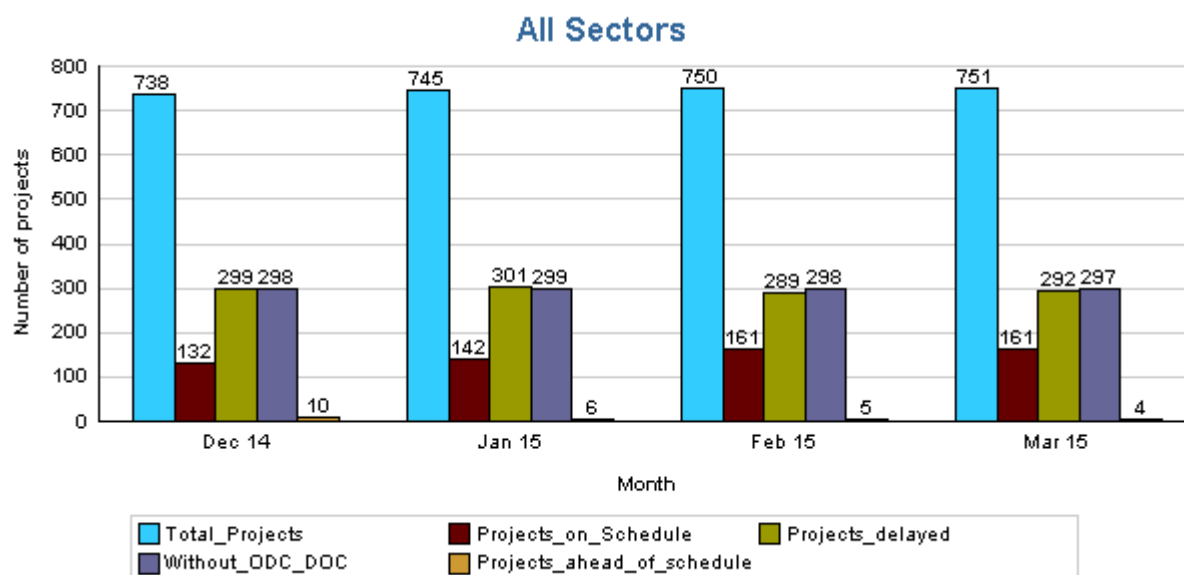


Break-up of 292 Delayed projects in March 2015

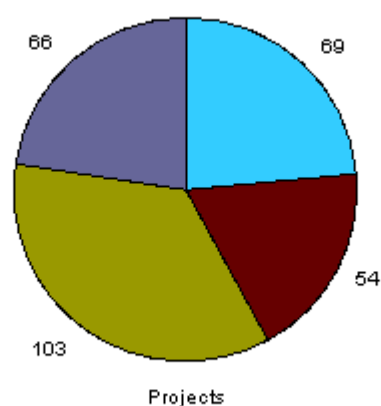


Delay in Months



Graphical Presentation of CIVIL AVIATION Sector

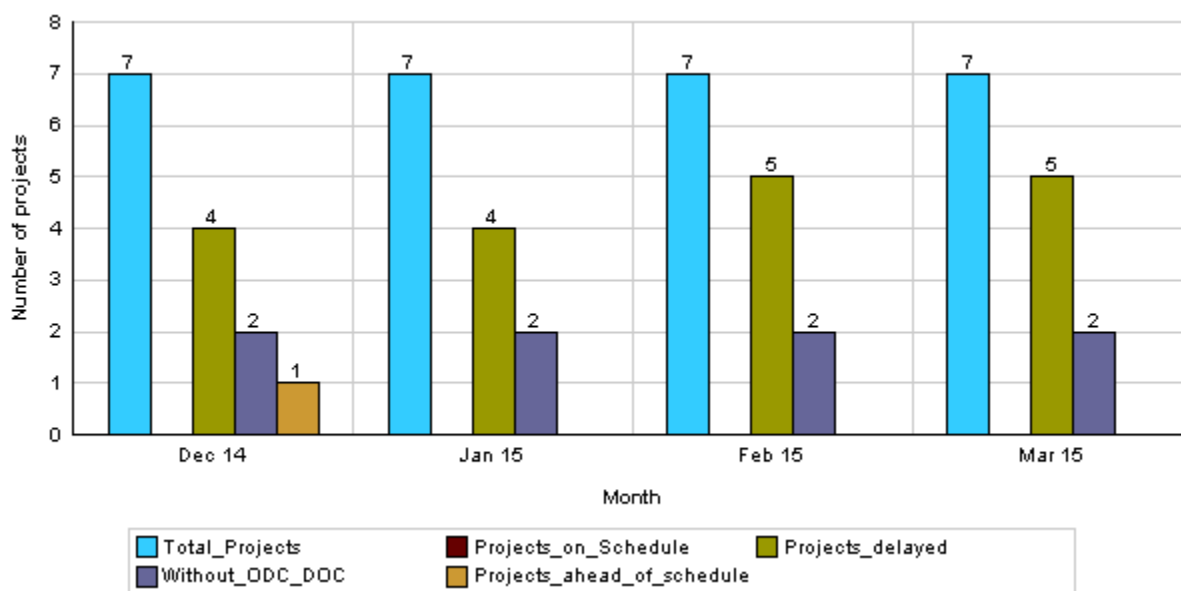


Break-up of 5 Delayed projects in March 2015

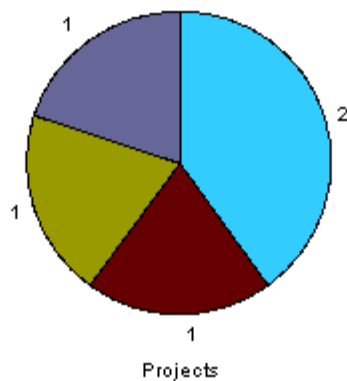


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Projects	2	1	1	1

Graphical Presentation of COAL Sector

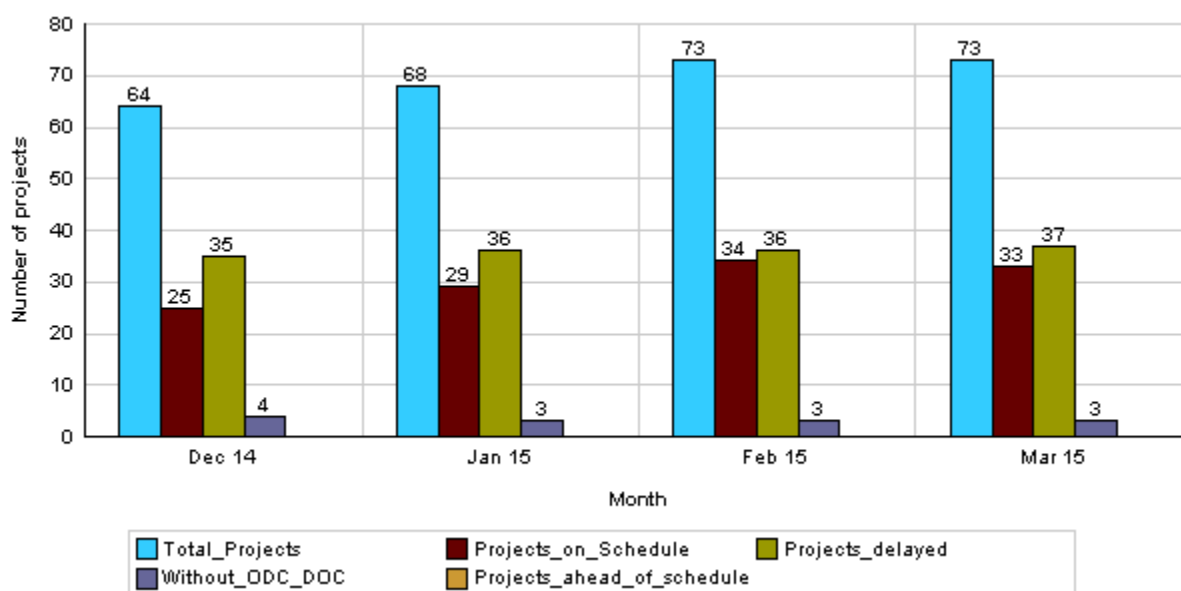


Break-up of 37 Delayed projects in March 2015

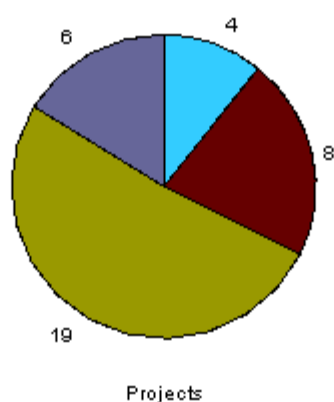

Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of MINES Sector

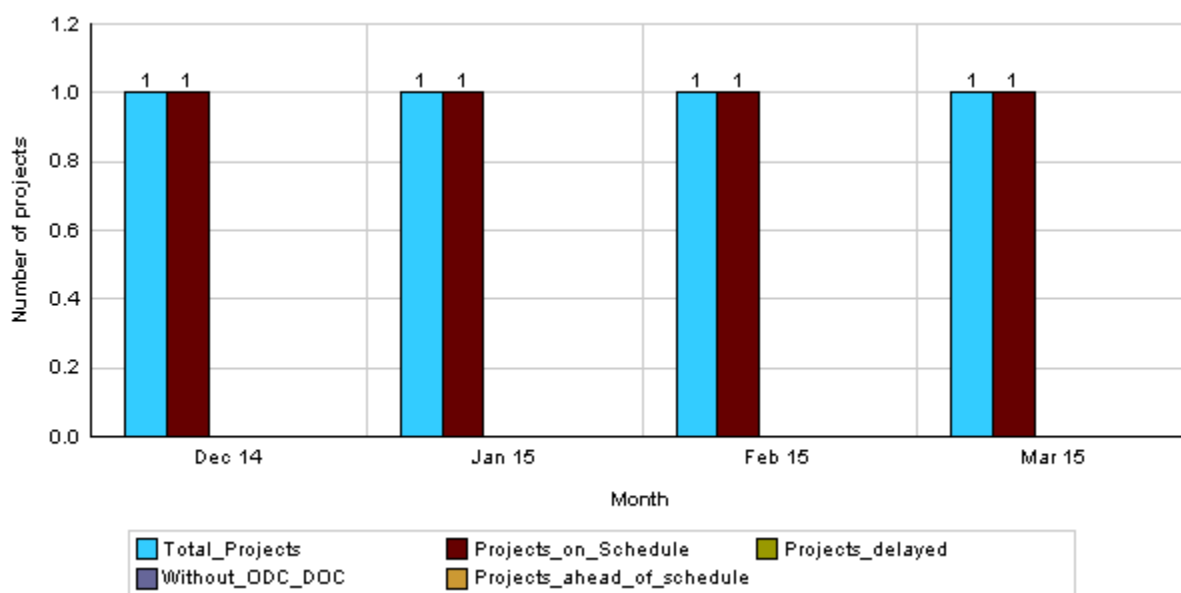


Break-up of 0 Delayed projects in March 2015


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	0	0	0	0
13-24	0	0	0	0
25-60	0	0	0	0
MORE THAN 60	0	0	0	0

Graphical Presentation of PETROLEUM Sector

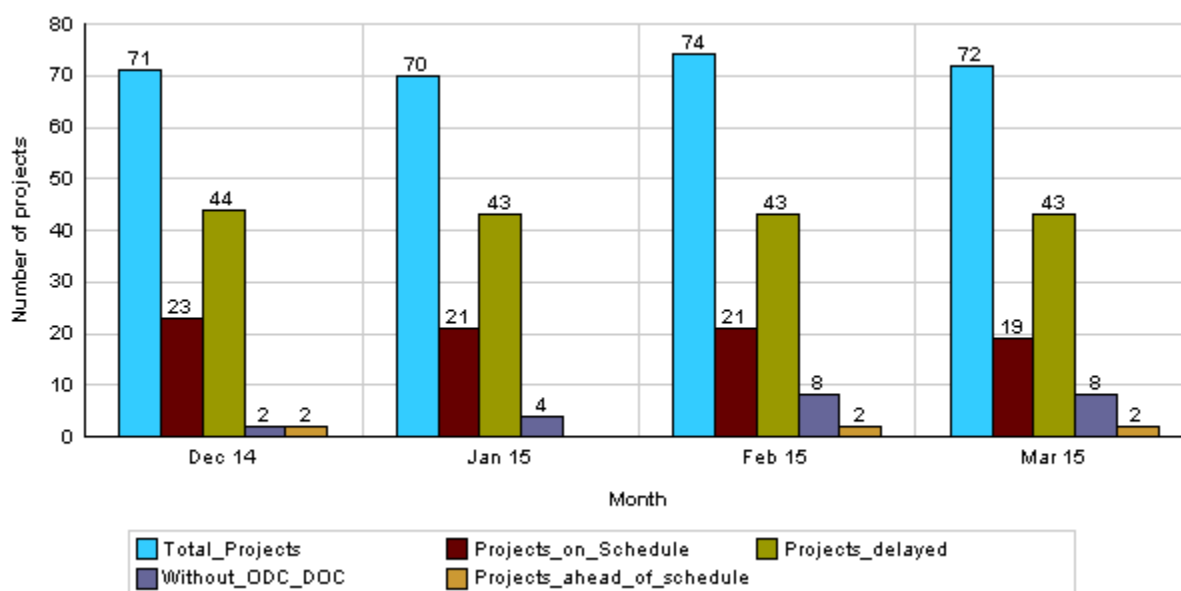


Break-up of 43 Delayed projects in March 2015

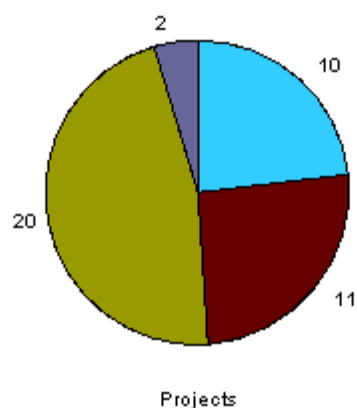


Delay in Months: 1-12, 13-24, 25-60, MORE THAN 60

Graphical Presentation of POWER Sector

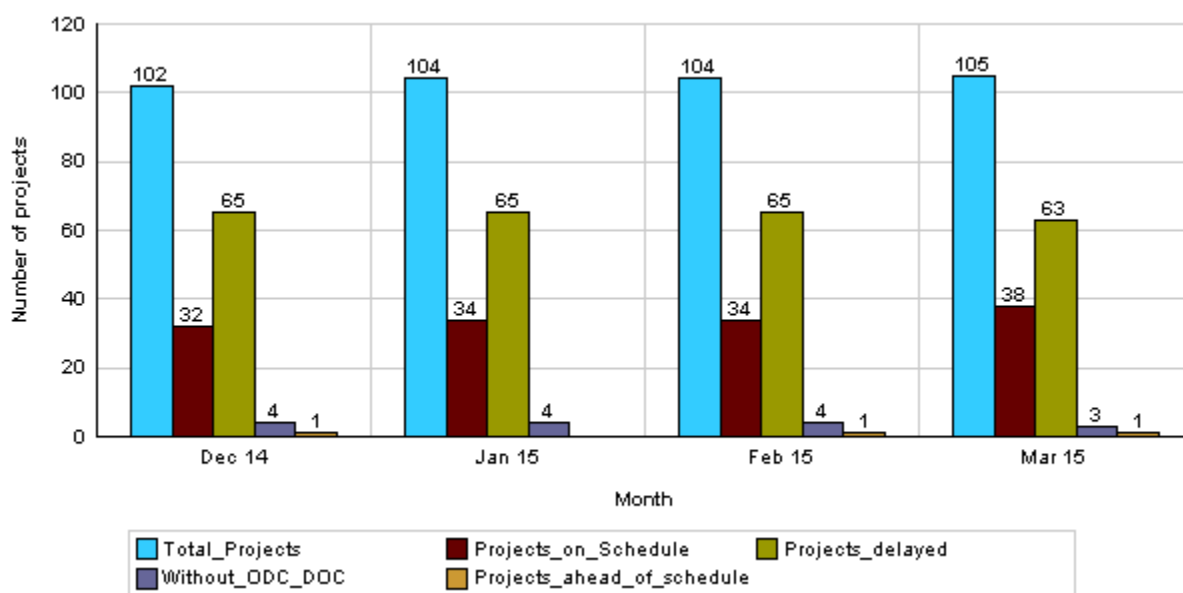


Break-up of 63 Delayed projects in March 2015

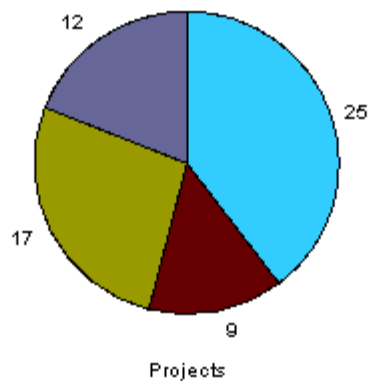


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of RAILWAYS Sector

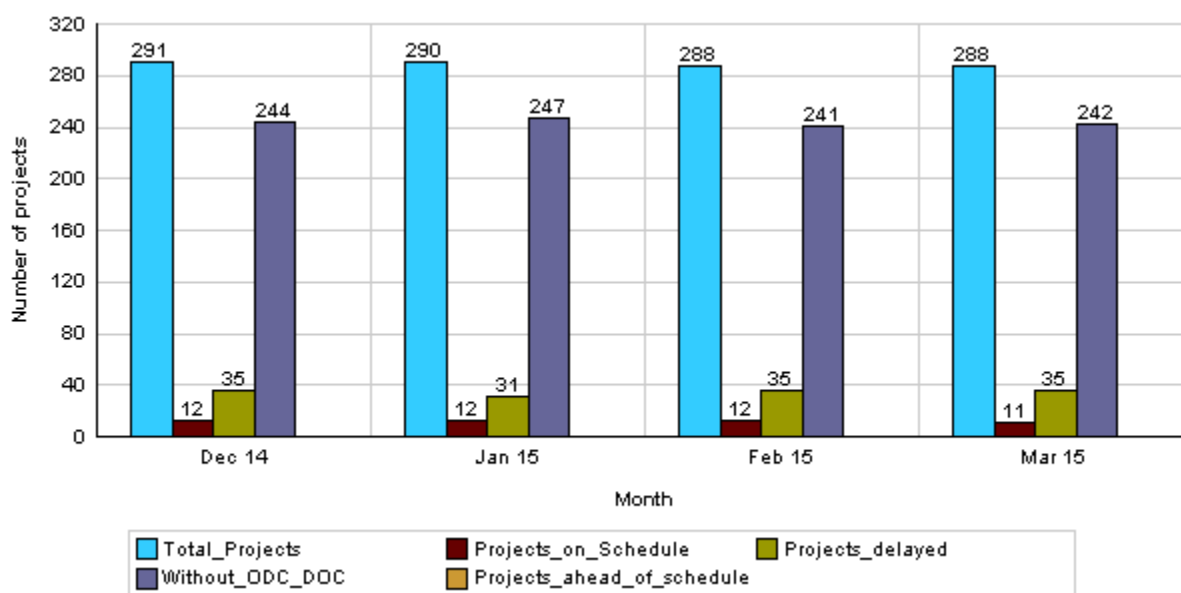


Break-up of 35 Delayed projects in March 2015

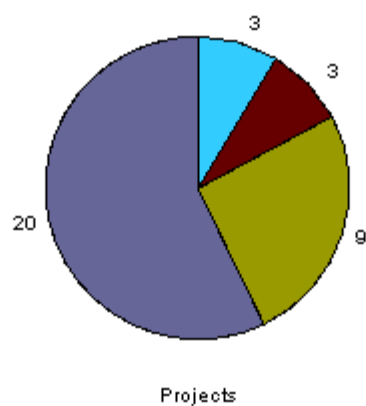


Delay in Months: 1-12 (Cyan), 13-24 (Dark Red), 25-60 (Olive Green), MORE THAN 60 (Purple)

Graphical Presentation of ROAD TRANSPORT AND HIGHWAYS Sector

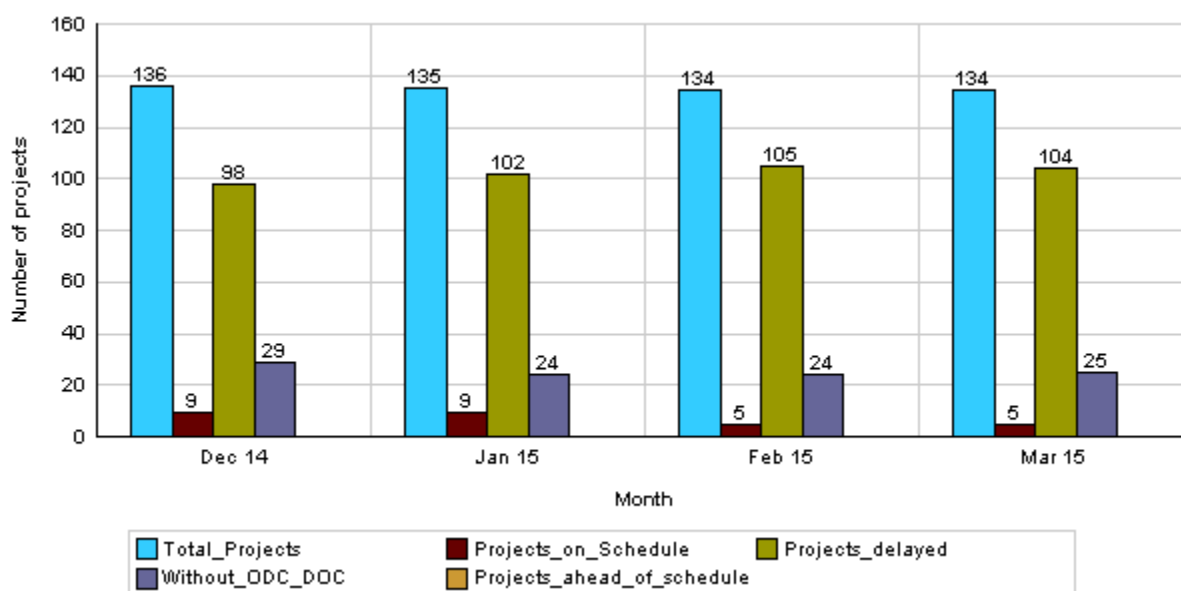


Break-up of 104 Delayed projects in March 2015

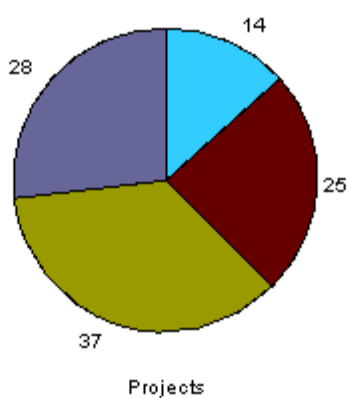


Delay in Months: 1-12 (Light Blue), 13-24 (Dark Red), 25-60 (Olive Green), MORE THAN 60 (Purple)

Graphical Presentation of ATOMIC ENERGY Sector

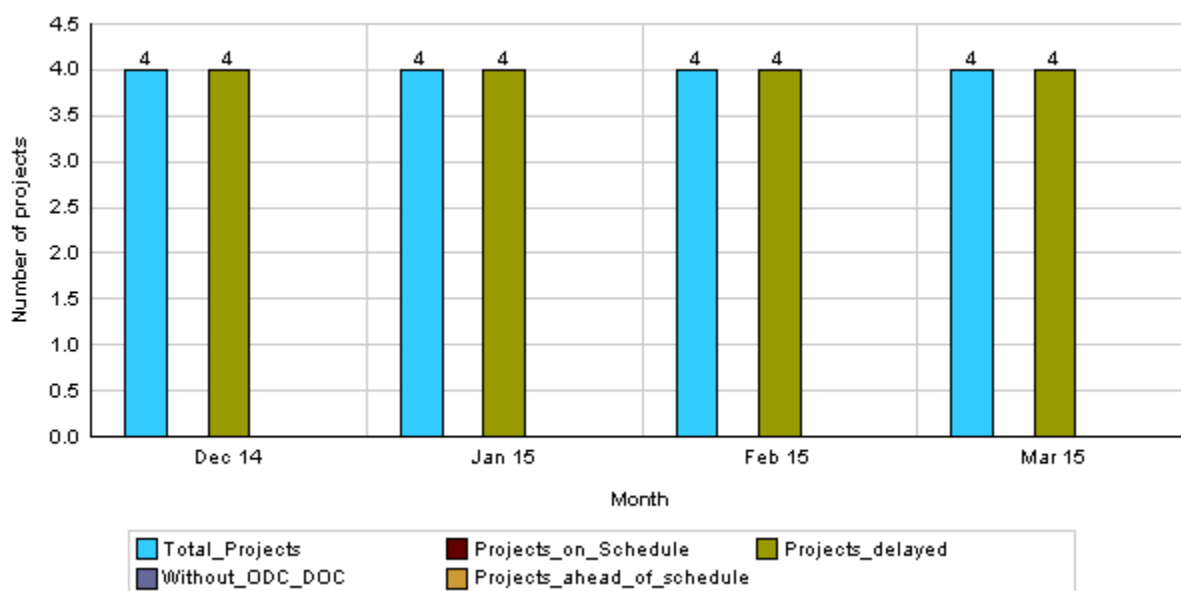

Break-up of 4 Delayed projects in March 2015

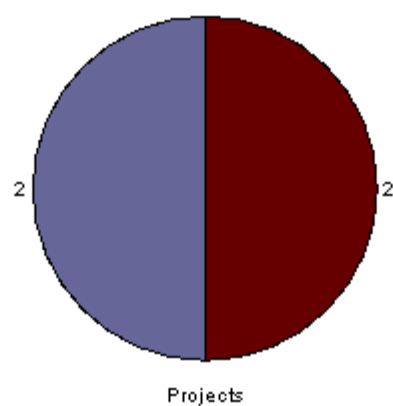


Delay in Months

Legend:

- 1-12
- 13-24
- 25-60
- MORE THAN 60

Graphical Presentation of SHIPPING AND PORTS Sector

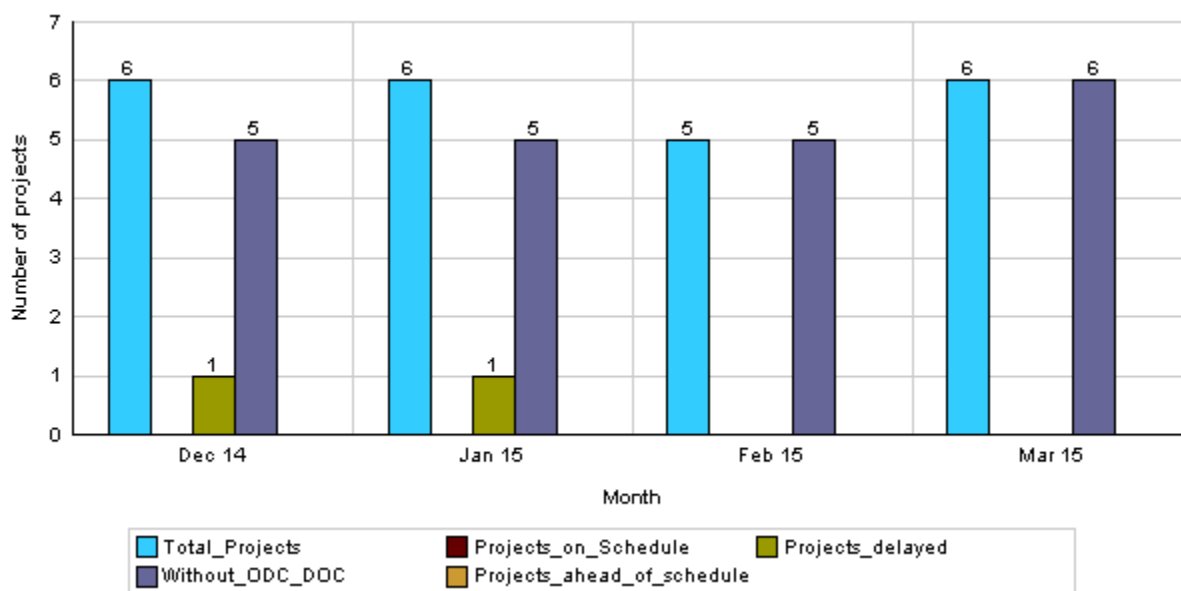


Break-up of 0 Delayed projects in March 2015


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	0	0	0	0
13-24	0	0	0	0
25-60	0	0	0	0
MORE THAN 60	0	0	0	0

Graphical Presentation of STEEL Sector

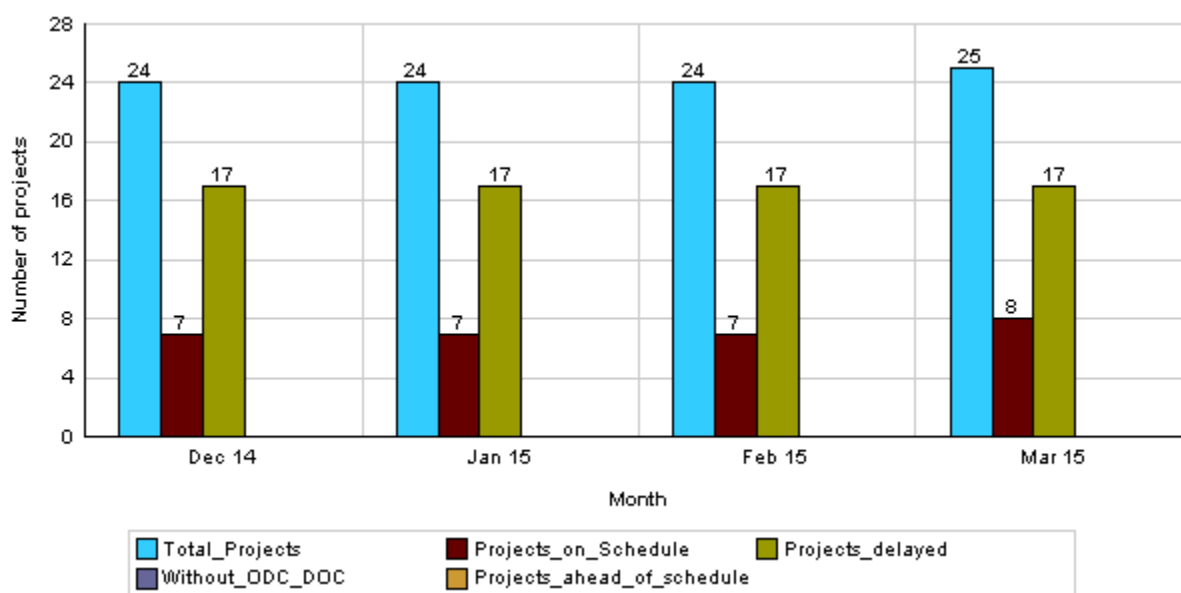


Break-up of 17 Delayed projects in March 2015

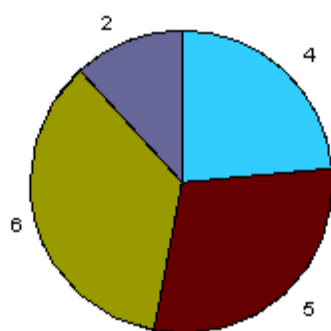


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Projects	4	5	6	2

Graphical Presentation of TELECOMMUNICATIONS Sector

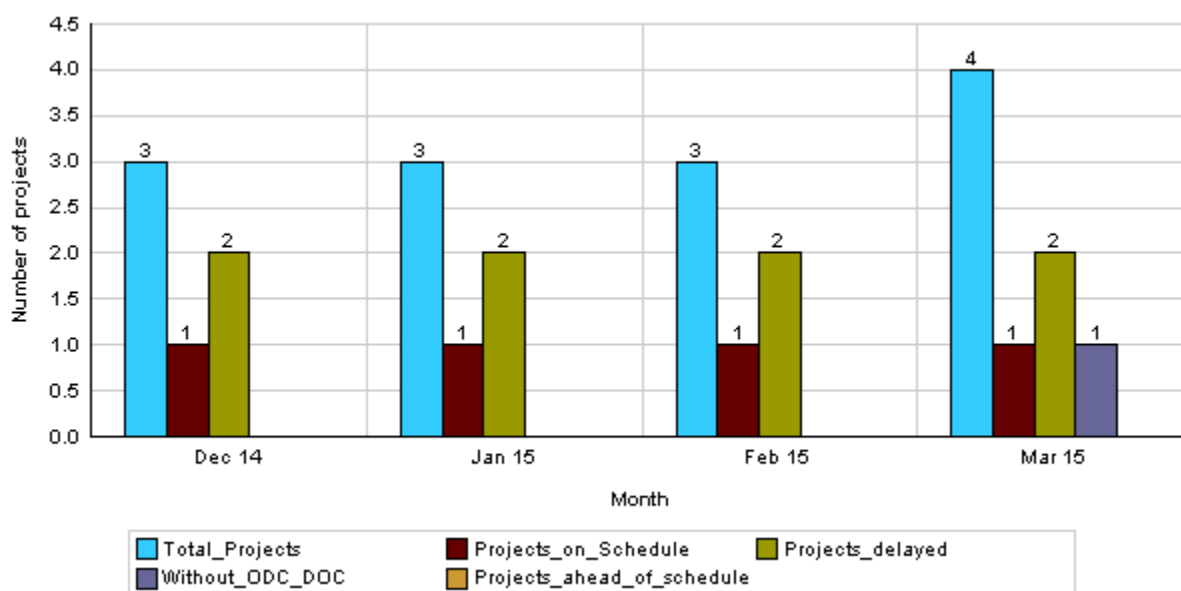


Break-up of 2 Delayed projects in March 2015

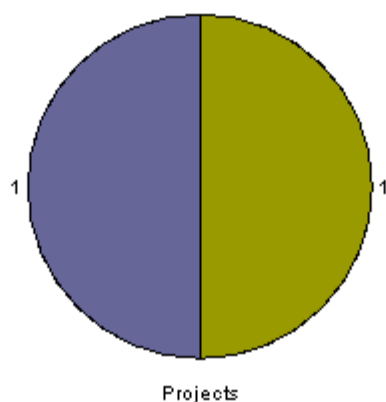


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Count	1	0	1	0

Graphical Presentation of URBAN DEVELOPMENT Sector

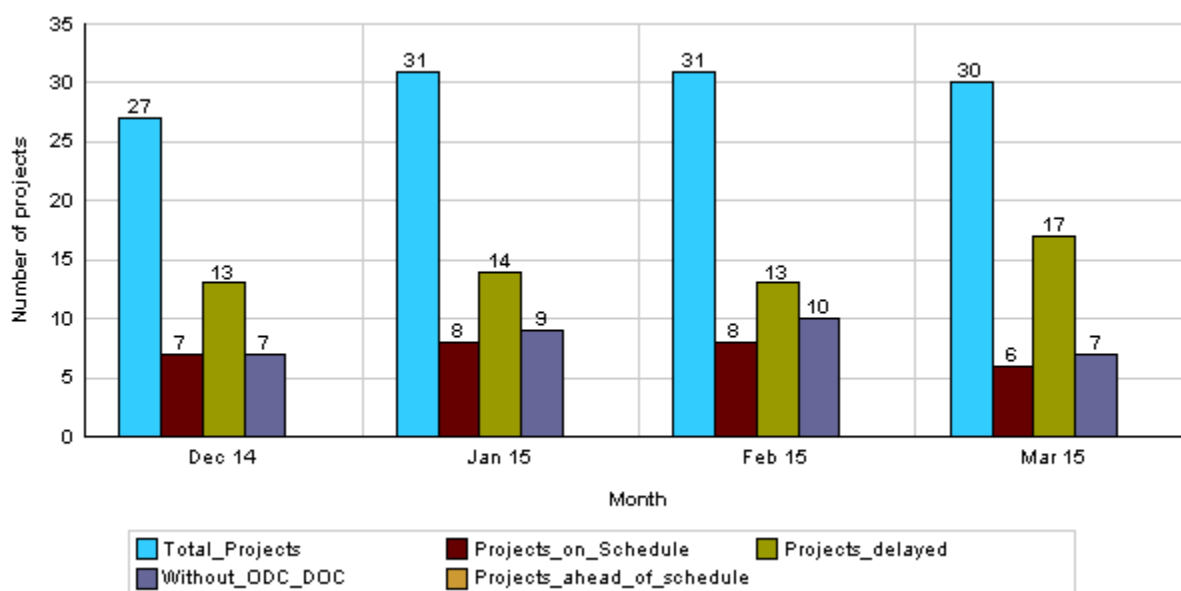

Break-up of 17 Delayed projects in March 2015

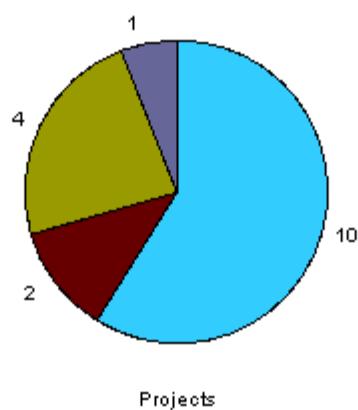

Delay in Months: 1-12, 13-24, 25-60, MORE THAN 60

Sectorwise analysis of projects					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	40,442.00	51,918.00	51,918.00	33,554.80
CIVIL AVIATION	7	2,599.56	2,636.56	2,652.48	1,629.30
COAL	73	58,516.59	62,097.62	55,939.62	21,079.83
FERTILISERS	1	197.79	197.79	197.79	12.09
MINES	1	1,856.00	1,856.00	1,856.00	0.00
STEEL	25	59,680.22	63,279.22	63,394.62	43,484.51
PETROCHEMICALS	1	5,460.61	8,920.00	9,834.00	8,459.13
PETROLEUM	72	157,335.33	172,377.56	174,867.00	74,378.94
POWER	105	279,607.51	299,768.10	316,945.69	154,014.86
RAILWAYS	288	163,518.20	176,325.78	289,824.76	94,332.06
ROAD TRANSPORT AND HIGHWAYS	134	100,051.44	100,165.39	101,992.83	88,192.55
SHIPPING AND PORTS	6	5,158.07	5,158.07	5,759.15	2,259.70
TELECOMMUNICATIONS	4	15,131.81	15,131.81	15,131.81	610.91
URBAN DEVELOPMENT	30	138,680.82	138,680.82	143,894.82	22,529.43
Grand total	751	1,028,235.95	1,098,512.72	1,234,208.57	544,538.11

(All Cost/ Expenditure in Rs. Crore)

Sector Wise Details									
(March 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	6,297.00	12/2015 -	10/2017	22(O) -	4/70
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00 22,462.00	22,462.00	18,271.00	12/2008 10/2013	07/2015	79(O) 21(R)	40/102
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 5,677.00	5,677.00	4,933.80	09/2010 09/2016	09/2016	72(O) 0(R)	12/88
4	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	4,053.00	12/2016 -	05/2018	17(O) -	4/69
	Total		40,442.00 -	51,918.00	33,554.80				60/329
	<u>CIVIL AVIATION</u>								
5	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	309.46	338.57	01/2011 -	06/2016	65(O) -	0/0
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	314.61	17.83	- -	09/2018	- -	0/0
7	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 -	388.53	295.43	05/2012 -	03/2015	34(O) -	0/0
8	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]AAI,CHANDIGARH	02/2011	452.00 489.00	452.00	410.25	03/2015 -	04/2015	1(O) -	0/0
9	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	344.28	52.48	03/2014 -	04/2015	13(O) -	0/0
10	GAGAN PROJECT - [N04000065]AAI,MULTI STATE	09/2008	626.00 -	626.00	514.70	06/2013 -	-	-	0/0
11	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	217.60	0.04	03/2015 -	09/2015	6(O) -	0/0
	Total		2,599.56 -	2,652.48	1,629.30				0/0
	<u>COAL</u>								
12	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,TELANGANA	12/2009	212.34 1,228.39	1,228.39	879.85	03/2013 09/2012	09/2015	30(O) 36(R)	21/22
13	AMERA OC RCE - [N06000123]SECL,CHHATISGARH	02/2015	335.97 -	335.97	30.30	03/2018 -	03/2018	0(O) -	0/0
14	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH	11/2009	150.59 -	198.59	94.90	03/2016 -	03/2016	0(O) -	3/7
15	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]NCL,MADHYA PRADESH	12/2009	1,352.04 -	1,143.54	778.29	03/2016 -	03/2016	0(O) -	0/4
16	AMRAPALI OC(12MTY) - [N06000103]CCL,JHARKHAND	02/2012	858.11 -	858.11	101.90	03/2020 -	03/2020	0(O) -	3/4

Sector Wise Details

(March 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
17	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH	02/2015	481.60 -	481.60	-	03/2023 -	03/2023	0(O) -	0/0
18	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	172.80	03/2012 -	03/2017	60(O) -	4/5
19	ASHOK EXPN OCP CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	471.66 341.63	341.63	117.84	03/2011 -	03/2017	72(O) -	2/5
20	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	148.02	03/2010 -	03/2017	84(O) -	2/4
21	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56 -	258.56	74.44	03/2016 -	03/2016	0(O) -	3/6
22	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA	05/2014	479.15 -	479.15	6.34	03/2019 -	03/2019	0(O) -	1/8
23	BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH	09/2008	203.82 -	203.82	-	03/2015 -	03/2015	0(O) -	1/6
24	BHANEAGAON OC - [N06000121]WCL,MAHARASHTRA	02/2015	187.94 -	187.94	20.59	03/2023 -	03/2023	0(O) -	0/12
25	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.10 -	490.10	186.68	03/2017 -	03/2017	0(O) -	3/11
26	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL,CHHATISGARH	05/2014	164.49 -	164.49	22.10	03/2020 -	03/2020	0(O) -	0/0
27	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,MADHYA PRADESH	06/2011	746.04 -	535.10	348.33	03/2015 -	03/2016	12(O) -	0/3
28	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH	12/2013	610.63 -	610.33	-	03/2022 -	03/2022	0(O) -	1/7
29	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35 -	462.35	273.72	03/2014 -	03/2016	24(O) -	2/9
30	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	35.68	03/2011 -	03/2016	60(O) -	0/4
31	DINESH OCP - [N06000118]WCL,MAHARASHTRA	11/2014	611.16 -	611.16	6.02	03/2020 -	03/2020	0(O) -	0/5
32	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,607.84	03/2014 -	03/2016	24(O) -	7/13
33	GARJANBAHAL OCP - [N06000117]MCL,ODISHA	11/2014	1,375.38 -	1,375.38	2.49	03/2021 -	03/2021	0(O) -	0/9
34	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,648.31	03/2014 -	03/2016	24(O) -	11/16
35	GOKUL - [N06000120]WCL,MAHARASHTRA	11/2014	267.67 -	267.67	68.35	03/2018 -	03/2018	0(O) -	0/5
36	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,ODISHA	02/2008	395.87 -	395.87	76.74	03/2015 -	03/2021	72(O) -	1/12
37	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	479.63	118.94	03/2013 -	03/2017	48(O) -	2/7
38	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA	05/2014	337.66 -	337.66	-	03/2019 -	03/2019	0(O) -	2/5
39	JAGANNATHPOR OC - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	152.43	21.55	03/2015 -	03/2017	24(O) -	1/7
40	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	447.06	29.03	03/2015 -	03/2018	36(O) -	4/31
41	JALLARAM SHAFT PROJECT - [N06000025]SCCL,TELANGANA	09/2007	467.78 -	467.78	2.85	03/2013 -	-	-	6/83
42	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL	11/2006	287.18 -	287.17	142.59	03/2011 -	03/2017	72(O) -	5/15

Sector Wise Details

(March 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
43	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	453.63	104.49	12/2012 -	03/2017	51(O) -	11/44
44	KALYANKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	417.33	11.41	07/2016 -	03/2017	8(O) -	4/39
45	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH	12/2014	371.04 -	371.04	30.24	03/2021 -	03/2021	0(O) -	0/0
46	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	162.21	03/2013 -	03/2017	48(O) -	3/9
47	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND	08/2011	988.35 -	988.35	6.84	04/2017 -	04/2017	0(O) -	0/0
48	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	69.64	03/2014 -	03/2017	36(O) -	2/4
49	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24(O) -	1/7
50	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]NCL,UTTAR PRADESH	06/2011	1,131.28 -	1,131.28	77.88	03/2018 -	03/2018	0(O) -	0/4
51	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	242.29	0.03	03/2015 -	03/2018	36(O) -	0/5
52	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,UTTAR PRADESH	06/2011	789.88 -	741.62	464.94	03/2013 -	03/2016	36(O) -	0/2
53	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA	06/2014	289.03 -	289.03	-	03/2018 -	03/2018	0(O) -	0/5
54	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	132.68	03/2010 -	03/2017	84(O) -	8/10
55	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH	08/2013	7,612.33 7,612.33	1,188.31	756.61	03/2023 03/2023	03/2023	0(O) 0(R)	1/16
56	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	469.78 -	706.40	53.38	07/2012 -	03/2016	44(O) -	0/3
57	MAKARDHOKRA I OC - [N06000119]WCL,MAHARASHTRA	09/2014	266.23 -	266.23	61.70	03/2021 -	03/2021	0(O) -	0/7
58	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	211.71	03/2014 -	03/2016	24(O) -	3/6
59	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	181.19	36.60	03/2012 -	03/2016	48(O) -	4/6
60	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015	0(O) -	0/0
61	MURAIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	-	04/2014 -	-	-	0/0
62	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 -	5,907.11	784.75	12/2015 04/2018	04/2018	28(O) 0(R)	10/35
63	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 -	259.40	12.52	03/2012 -	03/2016	48(O) -	0/2
64	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND	02/2014	555.52 -	555.52	6.84	03/2021 -	03/2021	0(O) -	0/0
65	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	75.71	03/2012 -	03/2017	60(O) -	1/3
66	PELMA OCP(15.00MTY) - [N06000045]SECL,CHHATISGARH	11/2014	1,624.59 1,624.59	1,624.59	0.46	03/2023 03/2023	03/2023	0(O) 0(R)	1/1
67	PENGANGA OCP(REVISED) - [N06000066]WCL,MAHARASHTRA	09/2014	441.82 -	441.82	98.00	03/2020 -	03/2020	0(O) -	0/7

Sector Wise Details

(March 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
68	PUANADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	186.69	03/2013 -	03/2015	24(O) -	2/2
69	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	55.48	03/2014 -	03/2016	24(O) -	3/9
70	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH	12/2014	357.80 -	357.80	106.44	03/2021 -	03/2021	0(O) -	0/0
71	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	223.68	03/2016 -	03/2016	0(O) -	2/4
72	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	418.97	326.51	03/2012 -	03/2016	48(O) -	0/2
73	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	162.76	2.48	03/2015 -	03/2015	0(O) -	4/29
74	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 -	430.14	69.91	03/2016 -	03/2016	0(O) -	6/39
75	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	6.56	06/2015 -	03/2016	9(O) -	4/51
76	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78 -	209.78	74.96	03/2015 -	03/2015	0(O) -	8/31
77	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	249.03	70.99	03/2012 -	-	-	25/42
78	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA	05/2014	3,756.36 -	3,756.36	0.65	03/2026 -	03/2026	0(O) -	3/14
79	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05 -	1,055.05	148.67	03/2018 -	03/2018	0(O) -	1/10
80	TALABIRA OCP - [N06000043]MCL,ODISHA	03/2008	447.72 -	447.72	52.36	03/2016 -	03/2020	48(O) -	0/11
81	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	149.41	03/2012 -	03/2016	48(O) -	2/4
82	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,TAMIL NADU	10/2004	2,030.78 3,027.59	3,477.21	3,185.95	06/2009 03/2013	04/2015	70(O) 25(R)	22/23
83	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	6,115.69	03/2012 05/2014	04/2015	37(O) 11(R)	27/39
84	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]NLC,TAMIL NADU	04/2012	364.75 -	364.75	128.27	10/2014 -	06/2015	8(O) -	6/11
	Total		58,516.59 -	55,939.62	21,079.83				249/861
	<u>FERTILISERS</u>								
85	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79 -	197.79	12.09	11/2016 -	11/2016	0(O) -	0/0
	Total		197.79 -	197.79	12.09				0/0
	<u>MINES</u>								
86	EXPANSION OF MALANJKHAND MINE- DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]HCL,MADHYA PRADESH	09/2011	1,856.00 -	1,856.00	-	09/2017 -	09/2017	0(O) -	0/0
	Total		1,856.00 -	1,856.00	.00				0/0

Sector Wise Details

(March 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>STEEL</u>								
87	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,KARNATAKA	04/2011	572.00 -	572.00	451.58	04/2013 09/2014	06/2015	26(O) 9(R)	17/18
88	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND	10/2013	245.67 -	245.67	32.31	05/2016 -	05/2016	0(O) -	1/3
89	3RD CONVERTER AND 4TH CASTER - [N12000088]RINL,ANDHRA PRADESH	07/2011	974.76 -	974.76	69.15	07/2016 -	07/2016	0(O) -	1/2
90	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,KARNATAKA	02/2011	898.55 -	898.55	379.57	05/2013 01/2015	08/2015	27(O) 7(R)	16/20
91	ALTERNATE GAS NETWORK AT BSL - [N12000093]SAIL,JHARKHAND	03/2015	255.19 -	255.19	-	03/2018 -	03/2018	0(O) -	0/0
92	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]RINL,MULTI STATE	07/2007	480.00 -	450.00	375.17	09/2009 05/2012	06/2015	69(O) 37(R)	1/1
93	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]NMDC,CHHATISGARH	01/2007	607.17 -	607.17	386.96	12/2011 01/2015	03/2015	39(O) 2(R)	20/20
94	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL,ANDHRA PRADESH	07/2011	877.73 -	877.73	164.04	07/2015 -	03/2016	8(O) -	0/2
95	CAPTIVE POWER PLANT - 2 - [N12000087]RINL,ANDHRA PRADESH	02/2011	677.00 -	677.00	509.41	09/2013 -	05/2015	20(O) -	0/1
96	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH - [N12000078]SAIL,CHHATISGARH	07/2012	332.65 -	332.65	172.77	08/2014 -	06/2015	10(O) -	3/4
97	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH	04/2014	188.93 -	188.93	16.95	04/2015 -	04/2015	0(O) -	1/3
98	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL,ODISHA	11/2011	254.55 -	254.55	123.28	11/2013 -	06/2015	19(O) -	2/4
99	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	14,300.13	03/2013 -	09/2015	30(O) -	31/35
100	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,JHARKHAND	05/2010	6,325.00 -	6,325.00	5,097.28	12/2011 -	05/2015	41(O) -	20/24
101	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,WEST BENGAL	08/2010	2,875.00 -	2,875.00	2,567.13	12/2012 -	05/2015	29(O) -	18/20
102	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL,ANDHRA PRADESH	10/2005	8,692.00 12,291.00	12,291.00	11,284.83	10/2009 10/2012	05/2015	67(O) 31(R)	69/70
103	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA	12/2011	187.33 -	187.33	149.44	10/2013 -	08/2015	22(O) -	2/5
104	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL,ODISHA	10/2012	160.48 -	160.48	118.88	09/2014 -	06/2015	9(O) -	1/2
105	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH	01/2010	15,525.00 -	15,525.00	6,655.07	05/2015 12/2016	12/2016	19(O) 0(R)	12/79
106	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]SAIL,WEST BENGAL	11/2012	313.05 -	313.05	205.93	06/2015 -	06/2015	0(O) -	2/3
107	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079]SAIL,ODISHA	06/2012	237.09 -	237.09	155.48	12/2014 -	08/2015	8(O) -	1/2
108	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	488.40	23.52	10/2016 -	10/2016	0(O) -	0/0

Sector Wise Details

(March 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
109	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL,ANDHRA PRADESH	05/2012	404.16 -	404.16	144.33	07/2015 -	03/2017	20(O) -	0/1
110	TURBO BLOWER - 5 - [N12000092]RINL,ANDHRA PRADESH	12/2009	280.00 -	280.00	2.00	09/2016 -	09/2016	0(O) -	0/1
111	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]SAIL,ODISHA	06/2014	708.91 -	708.91	99.30	04/2016 -	04/2016	0(O) -	2/2
	Total		59,680.22 -	63,394.62	43,484.51				220/322
	<u>PETROCHEMICALS</u>								
112	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,ASSAM	04/2006	5,460.61 8,920.00	9,834.00	8,459.13	04/2012 12/2013	06/2015	38(O) 18(R)	23/29
	Total		5,460.61 -	9,834.00	8,459.13				23/29
	<u>PETROLEUM</u>								
113	102 MW WIND POWER PROJECT - [N16000119]ONGC,RAJASTHAN	07/2010	1,106.00 678.02	678.02	405.00	06/2012 03/2015	03/2015	33(O) 0(R)	0/1
114	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]ONGC,MULTI STATE	03/2014	2,476.82 -	2,476.82	-	12/2018 -	12/2018	0(O) -	0/9
115	AHMEDABAD REDEVELOPMENT PROJECT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10 -	1,916.10	1,161.74	12/2014 -	12/2017	36(O) -	0/0
116	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63 -	2,189.63	1,035.48	12/2014 -	12/2018	48(O) -	0/0
117	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 -	2,378.89	1,768.09	03/2013 03/2015	03/2016	36(O) 12(R)	2/15
118	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,MULTI STATE	08/2011	586.00 -	586.00	295.67	08/2015 -	12/2015	4(O) -	0/12
119	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 -	1,823.00	-	- -	-	-	0/0
120	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]GAIL,ANDHRA PRADESH	07/2014	419.04 -	419.04	27.85	01/2017 -	01/2017	0(O) -	0/0
121	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	736.65	472.24	09/2011 12/2015	12/2015	51(O) 0(R)	0/0
122	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC,MULTI STATE	11/2010	331.20 -	269.10	190.04	08/2013 05/2015	05/2015	21(O) 0(R)	0/5
123	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	317.64 -	240.95	111.38	09/2012 04/2015	10/2015	37(O) 6(R)	0/5
124	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 -	188.89	2.00	01/2014 11/2017	11/2017	46(O) 0(R)	0/2
125	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	723.64	-	03/2013 06/2016	06/2016	39(O) 0(R)	0/0
126	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 761.68	761.68	728.35	05/2013 06/2014	03/2015	22(O) 9(R)	1/5
127	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA	12/2009	1,584.00 -	1,584.00	1,193.37	08/2015 -	12/2015	4(O) -	0/12

Sector Wise Details

(March 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
128	DEV OF G1 AND GS-15 (ONGCL) - [N160100231]ONGC,MULTI STATE	04/2003	429.82 3,955.21	3,955.21	3,439.48	04/2006 04/2016	06/2015	110(O) -10(R)	0/5
129	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,MAHARASHTRA	06/2007	3,248.78 5,633.44	6,000.00	5,925.40	08/2010 03/2012	05/2015	57(O) 38(R)	3/13
130	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 2,592.17	2,592.17	534.59	05/2014 03/2016	03/2016	22(O) 0(R)	0/21
131	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]ONGC,MULTI STATE	03/2010	4,550.40 6,638.94	6,638.94	2,306.51	03/2013 11/2014	02/2015	-	0/10
132	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC,MULTI STATE	04/2013	284.82 -	284.82	-	04/2015 04/2015	05/2017	25(O) 25(R)	0/5
133	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17 600.17	600.17	249.17	12/2014 05/2015	05/2015	5(O) 0(R)	0/8
134	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE	06/2010	2,523.00 2,523.00	2,523.00	1,019.79	01/2014 12/2015	12/2015	23(O) 0(R)	0/13
135	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]ONGC,MULTI STATE	10/2013	429.06 429.00	429.06	-	10/2014 10/2015	10/2015	12(O) 0(R)	0/0
136	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL, WEST BENGAL	03/2014	3,076.00 -	3,076.00	91.65	09/2017 -	09/2017	0(O) -	0/0
137	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL, TAMIL NADU	05/2013	711.00 -	711.00	4.80	- -	-	-	0/0
138	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]ONGC,MAHARASHTRA	03/2012	5,608.40 -	5,608.40	3,576.16	05/2015 -	05/2015	0(O) -	0/17
139	IMPROVED OIL RECOVERY OF B-173A FIELD - [N16000185]ONGC,MAHARASHTRA	01/2012	352.49 -	352.49	104.58	03/2014 -	03/2016	24(O) -	0/0
140	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]IOCL, ASSAM	02/2014	163.88 -	163.88	14.86	07/2016 -	07/2016	0(O) -	2/6
141	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	854.43	03/2015 05/2016	05/2016	14(O) 0(R)	0/17
142	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]ONGC,MAHARASHTRA	12/2012	3,513.07 4,619.94	4,619.94	0.47	02/2016 04/2017	04/2017	14(O) 0(R)	0/0
143	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE	05/2013	4,124.35 -	4,124.35	75.24	04/2016 04/2016	04/2016	0(O) 0(R)	0/6
144	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL, KERALA	03/2012	14,225.00 -	16,504.00	5,828.23	05/2016 -	05/2016	0(O) -	0/30
145	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE	01/2012	352.49 -	352.49	104.58	03/2014 04/2015	04/2015	13(O) 0(R)	0/3
146	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL, MULTI STATE	07/2009	7,596.18 -	7,596.18	17.06	01/2013 -	02/2019	73(O) -	0/0
147	JAIPUR-PANIPAT NAPTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL, MULTI STATE	02/2015	890.00 -	890.00	-	- -	-	-	0/0
148	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL, MULTI STATE	06/2009	2,915.00 -	2,915.00	1,339.14	12/2012 -	06/2015	30(O) -	0/14
149	KOTA JOBNER PIPELINE PROJECT - [N16000170]BPCL, RAJASTHAN	04/2011	276.26 -	276.27	241.63	12/2015 -	03/2015	-9(O) -	0/10
150	LPG TERMINAL AT KOCHI - [N16000171]IOCL, KERALA	12/2012	607.06 607.06	607.06	57.79	01/2016 04/2017	04/2017	15(O) 0(R)	11/48

Sector Wise Details

(March 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
151	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,KARNATAKA	02/2012	666.00 838.00	838.00	443.65	11/2015 11/2016	11/2016	12(O) 0(R)	24/29
152	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL,ODISHA	07/2009	199.75 -	239.73	181.45	07/2013 -	-	-	0/1
153	MARKETING TOP AT KORBA - [N16000186]IOCL,CHHATISGARH	01/2011	141.86 -	232.00	126.07	09/2016 -	12/2015	-9(O) -	0/12
154	MEHESANA REDEVELOPMENT PROJECT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	3,823.00	1,076.57	04/2015 12/2017	12/2017	32(O) 0(R)	0/0
155	MH NORTH REDEVELOPMENT PHASE III - [N16000188]ONGC,MAHARASHTRA	06/2014	5,706.47 5,813.25	5,813.25	300.65	05/2017 05/2017	05/2017	0(O) 0(R)	0/16
156	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL,TAMIL NADU	12/2012	279.00 -	279.00	142.28	12/2014 06/2015	07/2015	7(O) 1(R)	57/58
157	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	171.83	-	- -	-	-	0/0
158	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	913.00	379.89	08/2015 -	08/2015	0(O) -	0/0
159	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00 -	2,321.00	0.30	- -	-	-	0/0
160	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	-	- -	07/2018	- -	0/31
161	PARADIP REFINERY PROJECT - [N16000058]IOCL,ODISHA	02/2009	29,777.00 34,555.00	34,555.00	28,733.70	11/2012 11/2013	03/2015	28(O) 16(R)	87/100
162	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	1,087.70	09/2012 -	03/2016	42(O) -	6/7
163	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT	09/2011	202.25 -	160.16	39.42	07/2016 -	07/2016	0(O) -	5/12
164	PIPELINE REPLACEMENT PROJECT-3 - [N16000137]ONGC,MULTI STATE	04/2012	2,547.26 1,417.00	1,417.00	1,410.50	05/2014 05/2015	05/2015	12(O) 0(R)	0/0
165	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	3,150.00	96.36	09/2017 -	09/2017	0(O) -	0/0
166	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	215.66	-	06/2012 11/2015	11/2015	41(O) 0(R)	0/0
167	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 686.58	686.58	-	04/2015 04/2015	04/2015	0(O) 0(R)	0/0
168	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL,MAHARASHTRA	03/2012	1,419.00 -	1,419.00	1,108.86	12/2014 -	03/2015	3(O) -	0/20
169	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]IOCL,BIHAR	04/2013	480.00 -	480.00	23.70	02/2016 -	02/2016	0(O) -	1/6
170	RESID UPGRADEATION PROJECT - [N16000184]CPCL,TAMIL NADU	02/2011	3,110.36 -	3,110.36	508.71	11/2015 -	11/2015	0(O) -	36/52
171	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96 -	191.96	77.79	05/2015 -	12/2015	7(O) -	0/12
172	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS - [N16000181]ONGC,MULTI STATE	03/2013	2,913.10 -	2,913.10	9.72	05/2016 04/2018	04/2018	23(O) 0(R)	0/0
173	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL,GUJARAT	12/2011	160.00 -	160.00	2.32	02/2016 -	02/2016	0(O) -	0/0
174	REWARI KANPUR PIPELINE PROJECT - [N16000145]HPCL,MULTI STATE	02/2012	1,210.64 1,446.34	1,446.34	982.15	11/2015 -	11/2015	0(O) -	17/25

Sector Wise Details

(March 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
175	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	450.55	10.60	03/2017 -	03/2017	0(O) -	0/0
176	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	944.84	10/2011 -	10/2015	48(O) -	0/0
177	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,398.50	01/2012 -	10/2015	45(O) -	0/0
178	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,ANDHRA PRADESH	01/2006	672.00 1,178.35	1,178.35	1,099.88	10/2011 -	10/2015	48(O) -	0/0
179	SURAT PARADIP PIPELINE PROJECT - [N16000163]GAIL,MULTI STATE	10/2012	10,281.00 -	10,281.00	1.36	04/2015 -	04/2015	0(O) -	0/0
180	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM	03/2009	228.64 -	214.19	122.59	12/2016 -	12/2016	0(O) -	0/0
181	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]ONGC,TRIPURA	07/2008	288.04 253.66	253.66	218.56	08/2012 03/2015	03/2015	31(O) 0(R)	0/1
182	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 1,200.00	1,200.00	180.26	03/2015 11/2015	02/2016	11(O) 3(R)	0/5
183	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 462.79	462.79	215.01	10/2014 10/2016	10/2016	24(O) 0(R)	23/40
184	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	429.00	278.78	06/2011 03/2012	07/2015	49(O) 40(R)	13/20
	Total		157,335.33 -	174,867.00	74,378.94				288/739
	POWER								
185	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]NEEPCO,TRIPURA	07/2012	296.87 363.73	363.73	309.52	12/2014 -	05/2015	5(O) -	9/17
186	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 -	155.57	-	03/2016 -	05/2016	2(O) -	0/0
187	BARH STPP STAGE -II - [N18000047]NTPC,BIHAR	02/2008	7,341.04 -	7,341.04	8,594.00	10/2013 -	03/2015	17(O) -	20/20
188	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 15,095.67	15,095.67	10,750.00	12/2009 10/2014	03/2018	99(O) 41(R)	26/46
189	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 6,749.18	6,749.18	5,138.00	09/2011 -	03/2017	66(O) -	12/35
190	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	480.65	12/2015 -	12/2015	0(O) -	9/19
191	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,732.36	09/2014 -	06/2015	9(O) -	12/19
192	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	664.43	06/2015 -	12/2015	6(O) -	0/7

Sector Wise Details

(March 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
193	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,ANDHRA PRADESH	03/2012	206.44 -	206.44	43.97	06/2014 -	-	-	5/20
194	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	102.00	06/2015 -	06/2015	0(O) -	5/7
195	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	1,394.52	-	06/2017 -	06/2017	0(O) -	0/0
196	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA	02/2014	12,532.44 -	12,532.44	1,408.00	08/2018 -	08/2018	0(O) -	13/14
197	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 -	196.58	-	02/2016 -	02/2016	0(O) -	5/7
198	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	965.23	11/2012 -	03/2016	40(O) -	2/12
199	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	1,364.52	135.34	04/2016 -	04/2016	0(O) -	11/20
200	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 -	522.29	-	11/2016 -	11/2016	0(O) -	0/0
201	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	16.00	09/2014 -	06/2016	21(O) -	0/0
202	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	197.40	-	04/2018 -	04/2018	0(O) -	0/0
203	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATTISGARH	05/2011	1,961.87 -	1,961.87	1,653.45	05/2014 -	03/2015	10(O) -	5/11
204	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH	07/2013	3,363.12 -	3,363.12	510.00	12/2016 -	05/2017	5(O) -	12/15
205	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	03/2013	11,638.55 -	11,638.55	2,772.00	09/2017 -	09/2017	0(O) -	16/40
206	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,BIHAR	12/2011	901.77 1,025.28	1,025.28	867.80	08/2014 04/2015	04/2015	8(O) 0(R)	11/15
207	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]PGCIL,MULTI STATE	05/2014	303.07 -	303.07	1.00	07/2016 -	07/2016	0(O) -	0/0
208	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24 -	1,071.24	-	10/2017 -	10/2017	0(O) -	0/0
209	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154]PGCIL,MAHARASHTRA	10/2013	1,315.90 -	1,315.90	365.47	10/2016 -	03/2016	-7(O) -	8/17
210	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]PGCIL,MULTI STATE	12/2014	6,517.36 -	6,517.36	-	04/2018 -	04/2018	0(O) -	0/0
211	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,KARNATAKA	03/2005	1,007.16 -	1,007.16	970.31	12/2007 12/2009	12/2015	96(O) 72(R)	3/10
212	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 4,676.34	4,676.34	3,824.04	12/2009 03/2017	03/2017	87(O) 0(R)	13/29
213	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,497.72	3,915.36	01/2016 -	11/2016	10(O) -	4/6

Sector Wise Details

(March 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
214	KOLDAM HEP (NTPC) - [180100211]NTPC,HIMACHAL PRADESH	10/2002	4,527.15 7,220.00	7,220.00	6,544.00	04/2009 -	06/2015	74(O) -	8/9
215	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	01/2012	15,166.19 -	15,166.19	7,894.00	01/2017 -	03/2017	2(O) -	24/27
216	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	2,159.07	1,889.15	09/2008 03/2012	03/2016	90(O) 48(R)	17/23
217	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	12/2012	11,846.00 -	11,846.00	3,718.00	06/2017 -	06/2017	0(O) -	17/38
218	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	1,527.00	147.00	08/2017 -	08/2017	0(O) -	0/9
219	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	7,921.47	3,839.00	09/2016 -	02/2017	5(O) -	21/26
220	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 -	14,366.58	2,056.00	02/2019 -	02/2019	0(O) -	1/1
221	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	10,130.80	08/2013 -	03/2016	31(O) -	4/17
222	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL,MULTI STATE	02/2014	908.08 -	908.08	20.00	06/2016 -	06/2016	0(O) -	10/20
223	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 -	752.64	473.82	07/2013 -	12/2015	29(O) -	3/10
224	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	313.27	02/2012 -	03/2016	49(O) -	4/13
225	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	458.76	11/2011 -	03/2016	52(O) -	4/13
226	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 -	539.82	14.00	06/2016 -	06/2016	0(O) -	9/20
227	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,170.02	04/2013 -	03/2016	35(O) -	3/11
228	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	478.22	11/2014 -	12/2015	13(O) -	11/16
229	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL,MULTI STATE	09/2013	680.69 -	680.69	164.49	03/2016 -	03/2016	0(O) -	8/17
230	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]PGCIL,MULTI STATE	09/2012	803.34 -	803.34	544.89	03/2015 -	05/2015	2(O) -	13/17
231	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	171.92	04/2015 -	05/2015	1(O) -	11/18
232	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	719.74	11/2012 -	12/2015	37(O) -	2/11
233	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]NHPC,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	-	04/2020 -	04/2020	0(O) -	0/0
234	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	7,531.72	4,959.80	09/2009 -	12/2018	111(O) -	7/12
235	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99 1,487.49	1,487.49	994.41	08/2013 -	03/2016	31(O) -	26/37
236	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL	09/2014	1,381.84 -	1,381.84	109.00	09/2019 -	09/2019	0(O) -	2/2
237	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	4,571.00	11/2016 -	08/2017	9(O) -	19/22
238	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE	05/2014	829.98 -	829.98	-	08/2016 -	08/2016	0(O) -	0/0

Sector Wise Details

(March 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
239	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]PGCIL,KARNATAKA	02/2014	167.40 -	167.40	3.00	12/2015 -	12/2015	0(O) -	6/7
240	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]PGCIL,MULTI STATE	11/2014	972.42 -	972.42	-	11/2017 -	11/2017	0(O) -	0/0
241	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	15,300.00	7,576.36	09/2010 -	-	-	0/0
242	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]PGCIL,ANDHRA PRADESH	03/2015	550.06 -	550.06	-	04/2018 -	04/2018	0(O) -	0/0
243	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,MULTI STATE	09/2012	1,508.74 -	1,508.74	627.18	03/2015 -	12/2015	9(O) -	10/19
244	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE	08/2014	288.49 -	288.49	-	02/2017 -	02/2017	0(O) -	0/0
245	SYSTEM STRENGTHENING - XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	232.34	192.79	06/2012 -	-	-	1/3
246	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL,MADHYA PRADESH	03/2012	213.78 -	213.78	190.44	03/2014 -	03/2015	12(O) -	7/7
247	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 2,228.71	2,228.71	863.63	08/2014 -	05/2015	9(O) -	10/17
248	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,045.29	08/2012 -	03/2016	43(O) -	2/6
249	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]PGCIL,MULTI STATE	02/2014	243.53 -	243.53	44.00	08/2016 -	08/2016	0(O) -	10/20
250	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 -	203.28	-	07/2017 -	07/2017	0(O) -	0/0
251	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,MULTI STATE	06/2012	1,263.26 -	1,263.26	1,006.48	11/2014 -	06/2015	7(O) -	8/15
252	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATISGARH	01/2012	1,422.85 -	1,422.85	932.12	01/2015 -	12/2015	11(O) -	12/20
253	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 346.79	346.79	262.57	08/2014 06/2015	06/2015	10(O) 0(R)	13/19
254	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	487.49	336.42	06/2014 -	09/2015	15(O) -	15/19
255	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH	09/2014	9,188.98 -	9,188.98	578.00	03/2019 -	03/2019	0(O) -	5/5
256	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	2,420.00	03/2013 -	05/2018	62(O) -	1/14
257	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]NHPC, WEST BENGAL	09/2005	1,061.38 -	1,929.15	1,715.90	09/2009 -	06/2016	81(O) -	2/5
258	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	1,189.01	07/2010 02/2016	05/2018	94(O) 27(R)	5/21
259	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	1,801.76	08/2014 -	06/2015	10(O) -	12/19

Sector Wise Details

(March 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
260	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	2,195.41	10/2014 -	06/2015	8(O) -	8/17
261	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	4,041.48	10/2012 -	03/2016	41(O) -	1/11
262	TRANS. SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]PGCIL,MULTI STATE	06/2014	400.47 -	400.47	-	04/2017 -	04/2017	0(O) -	0/0
263	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	2,036.00	12/2012 -	03/2016	39(O) -	2/11
264	TRANS. SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]PGCIL,ANDHRA PRADESH	08/2014	188.75 -	188.75	-	02/2017 -	02/2017	0(O) -	0/0
265	TRANS.SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	5,151.37	442.00	03/2018 -	03/2018	0(O) -	0/20
266	TRANSM SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 -	4,404.57	1,221.75	01/2015 -	12/2015	11(O) -	8/21
267	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]PGCIL,GUJARAT	02/2014	378.71 -	378.71	34.00	10/2016 -	10/2016	0(O) -	6/20
268	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]PGCIL,MULTI STATE	01/2015	268.80 -	268.80	-	03/2018 -	03/2018	0(O) -	0/0
269	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL,MULTI STATE	02/2012	1,927.16 -	1,927.16	1,462.27	10/2014 -	04/2015	6(O) -	9/15
270	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL,MULTI STATE	09/2013	1,575.30 -	1,575.30	214.60	05/2016 -	05/2016	0(O) -	10/18
271	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE	01/2015	871.62 -	871.62	-	10/2017 -	10/2017	0(O) -	0/0
272	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	468.60	02/2014 -	09/2015	19(O) -	12/16
273	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]PGCIL,MULTI STATE	09/2011	1,366.34 1,606.38	1,606.38	1,268.66	12/2013 04/2015	04/2015	16(O) 0(R)	9/12
274	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	419.81	11/2013 -	12/2015	25(O) -	12/20
275	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 2,348.37	2,348.37	1,764.24	03/2013 06/2015	06/2015	27(O) 0(R)	6/14
276	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]PGCIL,MULTI STATE	03/2011	2,569.25 3,105.51	3,105.51	2,729.47	03/2014 06/2015	06/2015	15(O) 0(R)	8/14
277	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19 -	2,743.19	2,659.80	12/2013 -	09/2015	21(O) -	7/12

Sector Wise Details

(March 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
278	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	105.10	01/2013 -	06/2015	29(O) -	9/21
279	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,407.46	11/2013 -	06/2015	19(O) -	7/15
280	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. - [N18000076]PGCIL,MULTI STATE	03/2010	4,672.99 -	4,672.99	3,607.97	11/2012 -	07/2015	32(O) -	3/10
281	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH	11/2011	2,127.51 -	2,127.51	2,129.33	07/2014 -	05/2015	10(O) -	8/13
282	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 -	994.85	898.22	07/2013 02/2011	08/2015	25(O) 54(R)	24/26
283	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM	07/1998	368.72 1,381.71	1,381.71	800.74	07/2006 12/2015	10/2016	123(O) 10(R)	5/13
284	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	-	04/2016 -	04/2016	0(O) -	0/0
285	VINDHYACHAL STPP STAGE-V - [N18000134]NTPC,MADHYA PRADESH	05/2012	3,180.40 -	3,180.40	1,740.00	08/2015 -	08/2015	0(O) -	21/22
286	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	3,745.08	592.40	07/2014 11/2018	11/2018	52(O) 0(R)	2/8
287	WARDHA-HYDERABAD 765 KV LINK - [N18000183]PGCIL,MULTI STATE	01/2015	3,662.02 -	3,662.02	-	05/2018 -	05/2018	0(O) -	0/0
288	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 721.81	721.81	515.79	09/2010 06/2013	12/2015	63(O) 30(R)	0/7
289	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATISGARH	03/2012	9,569.76 -	9,569.76	3,874.59	06/2015 -	12/2015	6(O) -	15/28
	Total		279,607.51 -	316,945.69	154,014.86				736/1375
	<u>RAILWAYS</u>								
290	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP,TELANGANA	04/2012	632.68 -	816.55	42.58	03/2016 -	03/2018	24(O) -	0/0
291	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	184.06	15.23	- -	-	-	0/0
292	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 813.34	2,876.00	823.83	03/2014 -	03/2018	48(O) -	0/0
293	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	252.00 252.00	886.65	-	- -	03/2018	-	0/0
294	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	432.72	436.85	12/2009 03/2011	06/2015	66(O) 51(R)	0/0
295	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	567.18	31.99	- -	-	-	0/0
296	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	385.60	83.50	03/2013 -	-	-	0/0
297	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	2,820.00	329.67	- -	-	-	0/0

Sector Wise Details

(March 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
298	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	218.39	21.66	- -	-	-	0/0
299	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	822.00	-	- -	-	-	0/0
300	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE	04/2008	184.26 -	2,000.00	17.32	- -	-	-	0/0
301	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE	12/2006	170.00 -	485.00	417.70	03/2011 -	-	-	0/0
302	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	242.09	0.05	- -	-	-	0/0
303	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	338.54	129.14	- -	-	-	0/0
304	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	312.12 257.93	453.10	134.79	- -	03/2018	-	0/0
305	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 663.01	725.00	586.75	06/1999 -	07/2012	-	0/0
306	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	295.68	0.86	- -	-	-	0/0
307	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	307.00	-	- -	-	-	0/0
308	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	1,566.00	138.10	- -	-	-	0/0
309	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	490.80	0.39	- -	-	-	0/0
310	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	304.41	0.19	- -	-	-	0/0
311	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	528.00	2.96	- -	-	-	0/0
312	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	199.75	76.08	- -	-	-	0/0
313	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	986.30	88.13	- -	-	-	0/0
314	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	288.35	9.60	- -	-	-	0/0
315	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 -	207.52	223.44	12/2012 -	09/2015	33(O) -	0/0
316	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 -	1,382.78	2.76	- -	-	-	0/0
317	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	246.08	4.09	- -	-	-	0/0
318	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,WEST BENGAL	03/1998	111.90 1,039.29	2,371.85	486.25	03/2005 12/2008	12/2019	177(O) 132(R)	0/0
319	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	1,106.62 -	1,106.62	244.99	12/2010 -	-	-	0/0
320	BARIARPUUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	450.55	13.53	- -	-	-	0/0
321	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	255.64	-	- -	-	-	0/0

Sector Wise Details

(March 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
322	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP) - [220100164]MRTP, MAHARASHTRA	03/1996	495.44 495.44	1,781.98	420.45	03/2004 12/2010	03/2016	144(O) 63(R)	0/0
323	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR, MULTI STATE	04/2010	337.49 -	337.49	0.21	- -	-	-	0/0
324	BHADRACHALAM-KOVVUR - [N22000264]SCR, MULTI STATE	04/2012	923.23 -	923.23	1.01	- -	-	-	0/0
325	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR, ODISHA	03/2013	858.67 -	837.33	1.15	- -	-	-	0/0
326	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL	04/2011	289.64 -	760.00	0.09	- -	-	-	0/0
327	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	619.34 619.34	2,820.25	199.31	04/2014 03/2015	03/2018	47(O) 36(R)	0/0
328	BHANUPALI-BILASPUR BERI NL - [N22000273]NR, HIMACHAL PRADESH	04/2008	1,046.88 -	2,966.99	40.80	- -	-	-	0/0
329	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR, GUJARAT	04/2006	117.36 196.95	196.95	198.83	03/2011 -	-	-	0/0
330	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER, UTTAR PRADESH	03/2008	195.64 -	195.64	94.11	- -	-	-	0/0
331	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, MADHYA PRADESH	09/2007	687.20 -	800.00	798.47	03/2010 -	12/2015	69(O) -	0/0
332	BHUJ-NALIYA (GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR, GUJARAT	04/2008	318.24 -	321.62	2.91	03/2012 -	-	-	0/0
333	BIHTA-AURANGABAD (NL) - [N22000170]ECOR, BIHAR	04/2008	326.20 -	326.20	1.68	- -	-	-	0/0
334	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER, MULTI STATE	04/2011	175.80 -	175.80	1.46	- -	-	-	0/0
335	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	434.00	35.90	- -	-	-	0/0
336	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR, ASSAM	09/1997	1,500.00 1,000.00	4,996.19	3,410.06	04/2008 03/2014	06/2017	110(O) 39(R)	0/0
337	CALICUT-MANGALORE (DL) (SR) - [220100151]SR, MULTI STATE	02/1996	240.00 -	579.37	599.40	- -	02/2012	-	0/0
338	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER, ODISHA	04/2010	149.90 -	230.00	68.67	03/2015 -	12/2016	21(O) -	0/0
339	CHANDIGARH-BADDI NL - [N22000296]NR, MULTI STATE	04/2007	328.14 -	328.14	0.30	- -	-	-	0/0
340	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER, MULTI STATE	04/2003	337.96 -	337.96	61.36	- -	-	-	0/0
341	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR, TAMIL NADU	04/2007	247.00 -	951.24	619.87	- -	03/2015	- -	0/0
342	CHENGANNUR-CHINGAVANAM - [N22000203]SR, KERALA	04/2006	191.72 -	222.95	122.80	- -	-	-	0/0
343	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR, TAMIL NADU	04/1998	271.24 -	520.00	462.69	- -	-	-	0/0
344	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR, MULTI STATE	04/2008	523.52 -	1,200.00	2.07	- -	-	-	0/0

Sector Wise Details

(March 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
345	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	494.92	4.22	- -	-	-	0/0
346	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	378.56	111.69	- -	-	-	0/0
347	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 663.67	1,101.16	194.91	- -	03/2017	-	0/0
348	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	243.78	30.05	- -	-	-	0/0
349	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	367.77	-	- -	-	-	0/0
350	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	692.43	-	- -	-	-	0/0
351	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	595.91	89.60	- -	-	-	0/0
352	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	1,347.26	164.55	- -	-	-	0/0
353	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	573.78	166.84	- -	-	-	0/0
354	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR, TRIPURA	04/1999	895.00 575.00	1,242.25	1,005.81	03/2007 -	03/2016	108(O) -	0/0
355	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	556.64	268.56	- -	-	-	0/0
356	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	829.00	-	- -	-	-	0/0
357	CUTTACK - BARANG (LD) - [220100326]RVNL,ODISHA	04/1995	127.13 -	225.00	211.48	- 10/2014	10/2014	-	0/0
358	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	1,640.04	187.84	- -	-	-	0/0
359	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	533.38 -	533.38	114.38	12/2011 -	-	-	0/0
360	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL, CHHATISGARH	04/1995	304.00 -	968.60	150.78	12/2012 -	-	-	0/0
361	DANGOAPSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	583.00	144.66	12/2015 -	03/2016	3(O) -	0/0
362	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	406.92	155.87	- -	-	-	0/0
363	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	296.44	4.55	- -	-	-	0/0
364	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	205.00	5.20	- -	-	-	0/0
365	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	410.08	294.45	- -	-	-	0/0
366	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	234.71	137.01	03/2015 -	03/2015	0(O) -	0/0
367	DELHI-SOHNNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	1,239.00	-	- -	-	-	0/0
368	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	336.91	144.05	- -	-	-	0/0

Sector Wise Details

(March 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
369	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	607.09	561.14	12/2012 12/2012	-	-	0/0
370	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	376.59	4.58	- -	-	-	0/0
371	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 2,030.50	2,030.50	3.61	02/2019 -	02/2019	0(O) -	0/0
372	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 651.17	1,009.00	7.50	- -	12/2019	-	0/0
373	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	4,487.70	-	- -	-	-	0/0
374	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	914.98	846.18	- -	03/2015	-	0/0
375	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	4,874.58	2,371.00	03/2016 -	03/2016	0(O) -	0/0
376	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	272.39	141.55	03/2012 12/2013	03/2016	48(O) 27(R)	0/0
377	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	189.24	1.52	- -	-	-	0/0
378	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	603.22	1.64	- -	-	-	0/0
379	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 245.39	245.39	249.33	12/2008 -	10/2015	82(O) -	0/0
380	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	495.74	355.12	06/2013 06/2013	-	-	0/0
381	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N220000270]NR,UTTAR PRADESH	04/2013	654.00 -	654.00	-	- -	-	-	0/0
382	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	1,922.00	1.09	- -	-	-	0/0
383	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	270.00	301.84	02/2011 02/2011	-	-	0/0
384	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	415.67	13.98	- -	-	-	0/0
385	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	445.25	1.14	- -	-	-	0/0
386	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	197.73	-	- -	-	-	0/0
387	GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL	04/2009	611.03 -	611.03	140.48	12/2011 11/2013	11/2013	-	0/0
388	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	261.70 -	280.00	177.01	02/2006 -	-	-	0/0
389	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,UTTAR PRADESH	04/1997	863.23 -	1,072.51	888.87	- -	06/2015	-	0/0
390	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,157.54	1,544.40	590.26	03/1998 -	12/2019	261(O) -	0/0
391	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	156.65	53.00	- -	-	-	0/0

Sector Wise Details

(March 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
392	GUDUR-DURGARA JAPATNAM - [N22000265]SCR, ANDHRA PRADESH	04/2011	283.54 -	283.54	0.31	- -	-	-	0/0
393	GULBARGA-BIDAR, SCR(NL) - [220100254]SCR, KARNATAKA	02/1998	242.42 369.70	844.00	798.87	- 05/2009	03/2015	- 70(R)	0/0
394	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR, MULTI STATE	04/1986	158.77 608.02	608.02	602.10	03/1994 -	03/2015	252(O) -	0/0
395	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR, RAJASTHAN	04/2011	239.73 -	179.32	30.46	- -	-	-	0/0
396	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR, MULTI STATE	04/2011	1,176.09 3,845.60	3,845.60	2.33	02/2020 -	02/2020	0(O) -	0/0
397	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER, MULTI STATE	04/2000	157.17 -	157.17	76.90	- -	-	-	0/0
398	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR, BIHAR	04/2013	213.01 -	367.17	13.04	- -	-	-	0/0
399	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR, BIHAR	04/2003	528.65 -	324.66	221.63	- -	-	-	0/0
400	HANSDIHA-GODDA NL - [N22000236]ER, MULTI STATE	04/2011	267.09 -	267.09	1.50	- -	-	-	0/0
401	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER, MULTI STATE	04/2010	172.03 -	172.03	5.86	- -	-	-	0/0
402	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, ODISHA	04/1996	301.64 -	1,185.64	334.04	- 09/2009	-	-	0/0
403	HARIDWAR-LAKSAR - [N22000289]NR, UTTARAKHAND	04/2012	219.83 -	329.97	2.38	- -	-	-	0/0
404	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR - [220100183]SWR, KARNATAKA	02/1997	295.00 -	1,289.92	1,060.40	- -	-	-	0/0
405	HATHUA-BHATNI (N L) (NER) - [220100319]NER, MULTI STATE	04/2005	230.03 -	230.03	172.58	- -	-	-	0/0
406	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR, RAJASTHAN	04/2008	829.74 -	829.74	93.08	03/2015 -	03/2015	0(O) -	0/0
407	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR, HARYANA	04/2013	400.00 -	400.00	-	- -	-	-	0/0
408	HOSADURGA - CHICKJAJUR (28.89 KM) - [N22000324]SWR, KARNATAKA	04/2010	203.40 -	203.40	142.86	- -	-	-	0/0
409	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR, KARNATAKA	04/2010	2,127.00 -	2,127.00	282.11	- -	-	-	0/0
410	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER, MULTI STATE	04/2010	157.94 -	157.94	43.34	- -	-	-	0/0
411	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, WEST BENGAL	04/1974	393.46 393.46	1,026.00	181.48	03/2007 03/2007	03/2015	96(O) 96(R)	0/0
412	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER, MULTI STATE	04/2011	166.89 -	166.89	0.02	- -	-	-	0/0
413	HUBLI-ANKOLA(NL), SWR - [220100193]SWR, KARNATAKA	04/1997	227.00 997.58	2,135.00	117.11	- -	-	-	0/0
414	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR, MULTI STATE	04/2007	313.24 -	313.24	230.62	01/1999 -	-	-	0/0
415	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR, RAJASTHAN	04/2008	653.19 -	653.55	252.11	03/2014 -	-	-	0/0

Sector Wise Details

(March 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
416	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	162.96	143.62	- -	-	-	0/0
417	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	847.75	835.14	06/2007 -	-	-	0/0
418	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 501.69	1,043.56	802.58	03/2012 -	-	-	0/0
419	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	470.00	19.44	- -	-	-	0/0
420	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	230.00	218.67	- -	-	-	0/0
421	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	740.00	639.77	03/2012 03/2012	12/2012	-	0/0
422	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 727.56	6,570.75	2,787.99	03/2011 03/2014	03/2019	96(O) 60(R)	0/0
423	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	2,050.00	194.45	- -	-	-	0/0
424	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	923.52	208.10	- -	-	-	0/0
425	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	174.56	63.08	- -	-	-	0/0
426	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	279.70	4.73	- -	-	-	0/0
427	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,062.36	1,651.54	1,621.40	- -	03/2015	-	0/0
428	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	643.00	-	- -	-	-	0/0
429	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	744.71 -	744.71	576.86	- -	03/2016	-	1/1
430	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	800.00	800.66	- -	-	-	0/0
431	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM	04/1998	227.90 200.00	331.40	182.22	12/2012 -	03/2016	39(O) -	0/0
432	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	1,727.27	743.74	12/2010 -	03/2018	87(O) -	0/0
433	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66 -	423.66	263.01	03/2017 -	03/2017	0(O) -	0/0
434	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 -	1,054.35	7.96	- -	-	-	0/0
435	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	162.87	146.82	- -	-	-	0/0
436	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	276.00	284.12	03/2009 03/2009	08/2014	-	0/0
437	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	1,995.25	355.02	- -	-	-	0/0
438	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 -	1,143.60	189.12	- -	03/2018	-	0/0

Sector Wise Details

(March 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
439	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	282.92 282.92	565.13	2.80	- 03/2014	03/2018	- 48(R)	0/0
440	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87 -	768.87	567.94	- 03/2010	03/2010	-	0/0
441	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	2,957.21 -	2,957.21	1,857.31	07/2005 -	-	-	0/0
442	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	418.17	237.93	- -	-	-	0/0
443	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE	04/2013	723.00 -	723.00	-	- -	-	-	0/0
444	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	341.41	325.92	03/2012 -	-	-	0/0
445	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	1,047.00	1.29	- -	-	-	0/0
446	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	252.96	1.52	- -	-	-	0/0
447	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	192.56	0.38	- -	-	-	0/0
448	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	346.15	14.82	- -	-	-	0/0
449	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	406.99	141.55	- -	-	-	0/0
450	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	1,630.97	488.76	05/2008 -	-	-	0/0
451	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	257.42	67.97	03/2014 -	03/2014	-	0/0
452	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM	04/2012	246.07 246.07	364.06	0.30	- -	03/2019	- -	0/0
453	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 -	5,500.00	4,734.45	03/2009 -	03/2016	84(O) -	0/0
454	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	480.00	3.51	07/2008 -	07/2008	-	0/0
455	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	450.00	16.97	- -	-	-	0/0
456	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	800.00	0.69	- -	-	-	0/0
457	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	493.96	121.27	- -	-	-	0/0
458	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	343.00	216.17	- -	-	-	0/0
459	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	900.05	853.83	12/2011 12/2010	-	-	0/0
460	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	378.56 -	791.59	5.41	- -	-	-	0/0
461	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 315.13	365.00	2.52	- -	12/2017	- -	0/0

Sector Wise Details

(March 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
462	MANSI-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	369.00	108.93	- -	-	-	0/0
463	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 332.92	477.88	488.87	03/2012 -	-	-	0/0
464	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	1,112.00	-	- -	-	-	0/0
465	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	279.54	2.74	01/1999 -	-	-	0/0
466	MAVLI JN.-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	855.16	557.72	- -	-	-	0/0
467	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	1,383.45	457.88	- -	-	-	0/0
468	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	377.44	7.50	- -	-	-	0/0
469	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	439.88	0.78	- -	-	-	0/0
470	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	800.00	0.83	01/1999 -	-	-	0/0
471	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	426.00	-	01/1999 -	-	-	0/0
472	MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	250.93	0.14	- -	-	-	0/0
473	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	211.00	4.41	- -	-	-	0/0
474	MUDKHED-PARBHANI - [N22000283]SCR,MAHARASHTRA	04/2011	390.60 -	390.60	4.69	- -	-	-	0/0
475	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 6,213.84	6,821.29	2,217.14	03/2014 03/2019	03/2019	60(O) 0(R)	0/0
476	MUNEERABAD-MAHABOONAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 236.41	645.00	309.19	- -	03/2015	-	0/0
477	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	1,350.91	339.53	- -	-	-	0/0
478	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	165.82 165.82	435.58	0.56	- -	03/2018	-	0/0
479	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	281.30	0.58	- -	-	-	0/0
480	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	228.05	0.05	- -	-	-	0/0
481	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	1,313.48	5.13	- -	-	-	0/0
482	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	883.00	755.50	02/2009 -	03/2015	73(O) -	0/0
483	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	2,100.00	391.95	07/2012 -	-	-	0/0
484	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	620.57	-	- -	-	-	0/0
485	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	494.54	31.20	- -	-	-	0/0

Sector Wise Details

(March 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
486	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	300.00 300.00	827.73	53.52	- -	03/2019	- -	0/0
487	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	200.00 200.00	496.24	213.72	- -	03/2017	- -	0/0
488	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 171.00	679.57	40.41	- -	03/2018	- -	0/0
489	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	4,083.02 -	5,307.90	7.79	- 03/2016	03/2020	- 48(R)	0/0
490	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 210.00	394.28	233.46	- -	03/2017	- -	0/0
491	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL	04/2010	221.42 205.31	563.13	22.39	- -	03/2019	- -	0/0
492	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	36.80 36.38	1,336.57	255.55	- -	03/2019	- -	0/0
493	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 1,798.00	1,887.90	-	- -	03/2019	- -	0/0
494	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR,WEST BENGAL	04/2011	209.77 190.39	441.45	85.78	- -	03/2018	- -	0/0
495	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR,WEST BENGAL	04/2012	283.55 278.21	288.81	11.74	- -	03/2018	- -	0/0
496	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NFR,MULTI STATE	04/1999	523.17 380.60	1,653.55	1,040.11	- -	03/2018	- -	0/0
497	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00 -	2,973.42	10.44	03/2015 03/2020	03/2020	60(O) 0(R)	0/0
498	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	733.00 733.00	2,531.34	1,732.43	12/2008 -	03/2018	111(O) -	0/0
499	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	2,069.60	34.87	03/2014 -	03/2016	24(O) -	0/0
500	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	2,619.02	525.84	03/2016 -	03/2016	0(O) -	0/0
501	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL,WEST BENGAL	04/2010	2,397.72 -	2,397.72	143.73	03/2016 -	06/2016	3(O) -	0/0
502	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	3,951.98	584.90	03/2016 -	03/2016	0(O) -	0/0
503	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	1,117.11	465.19	03/2008 06/2008	-	-	0/0
504	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT	04/2013	1,266.89 -	1,266.89	-	- -	-	-	0/0
505	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER,WEST BENGAL	04/2004	293.74 -	293.74	140.08	12/2010 -	-	-	0/0

Sector Wise Details

(March 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
506	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	96.16 -	260.16	240.21	- -	01/2015	-	0/0
507	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 -	2,921.00	2,339.60	10/2007 12/2012	12/2015	98(O) 36(R)	0/0
508	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 -	925.30	712.02	- -	02/2014	-	0/0
509	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	98.74 -	203.00	227.84	- -	03/2015	-	0/0
510	PIRAPINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	261.38	21.21	- -	-	-	0/0
511	PIRAPINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	915.98	0.09	- -	-	-	0/0
512	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 -	248.07	29.10	03/2015 -	03/2015	0(O) -	0/0
513	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	299.60	1.10	03/2017 -	03/2017	0(O) -	0/0
514	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	323.00	-	- -	-	-	0/0
515	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	205.22	1.54	- -	-	-	0/0
516	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	1,030.00	804.20	01/1999 -	-	-	0/0
517	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE	03/1998	280.00 -	1,122.00	889.95	- -	-	-	0/6
518	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	289.93	284.82	12/2007 03/2010	-	-	0/0
519	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 -	2,363.00	1,548.90	03/2009 12/2012	12/2014	-	0/0
520	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	288.00	311.89	02/2009 02/2009	08/2014	-	0/0
521	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	209.00	2.64	12/2016 -	12/2016	0(O) -	0/0
522	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 913.48	913.48	457.67	- -	-	-	0/0
523	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	874.57	703.56	03/2013 -	09/2015	30(O) -	0/0
524	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	470.92 727.13	1,225.90	257.59	- -	03/2017	-	0/0
525	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	335.00	230.67	06/2004 -	12/2015	138(O) -	0/0
526	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]NFR,ASSAM	01/2004	915.70 915.70	3,700.00	3,198.30	- -	03/2015	-	0/0
527	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	288.97	0.62	- -	-	-	0/0
528	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	872.22	794.55	- -	-	-	0/0
529	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	3,500.00	49.60	- -	-	-	0/0

Sector Wise Details

(March 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
530	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	1,421.25	420.33	03/2012 -	-	-	0/0
531	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	1,743.00	336.05	-	-	-	0/0
532	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	576.18	3.40	-	-	-	0/0
533	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTD,MAHARASHTRA	04/2012	714.10 -	714.10	59.18	04/2016 -	03/2017	11(O)	0/0
534	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	193.44	53.01	-	-	-	0/0
535	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	325.00	252.75	-	-	-	0/0
536	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	355.81	306.39	-	-	-	0/0
537	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	385.54	233.44	03/2010 -	-	-	0/0
538	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	155.81	18.25	-	-	-	0/0
539	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 -	1,111.99	60.31	-	-	-	0/0
540	SANTOSHAPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	268.52	78.81	-	-	-	0/0
541	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 1,339.48	4,190.00	88.56	12/2015 -	03/2020	51(O)	0/0
542	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	832.47	0.94	-	-	-	0/0
543	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	678.62	17.17	-	-	-	0/0
544	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	297.47	51.82	-	-	-	0/0
545	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	277.28	67.82	-	-	-	0/0
546	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	466.65	0.02	-	-	-	0/0
547	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	1,500.00	0.01	-	-	-	0/0
548	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	818.29	116.37	02/2015 -	02/2015	-	0/0
549	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	450.00	7.91	-	-	-	0/0
550	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 732.06	516.23	588.24	03/2014 -	-	-	0/0
551	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	810.80	160.80	-	-	-	0/0
552	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 1,013.74	1,428.00	466.36	06/2005 07/2011	12/2019	174(O) 101(R)	0/0

Sector Wise Details

(March 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
553	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	171.02 -	171.00	166.84	06/2013 -	01/2015	-	0/0
554	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	365.17	1.35	- -	-	-	0/0
555	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	1,188.91	687.63	- 12/2009	-	-	0/0
556	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR,TAMIL NADU	04/2011	190.10 -	190.10	33.19	- -	-	-	0/0
557	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	262.00	-	- -	-	-	0/0
558	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 -	1,080.00	194.61	- -	-	-	0/0
559	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 -	490.00	67.57	- -	-	-	0/0
560	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	167.73	124.14	03/2012 -	-	-	0/0
561	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 -	980.00	596.66	- -	-	-	0/0
562	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL	03/2000	1,049.69 3,385.14	3,404.92	3,538.88	12/2006 -	-	-	0/0
563	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	167.50	0.32	- -	-	-	0/0
564	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	1,801.01	1.13	- -	-	-	0/0
565	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	19,565.00	10,658.34	11/2002 -	12/2018	193(O) -	0/0
566	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	1,389.62	1,055.80	03/2014 -	-	-	0/0
567	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	380.00	1.38	- -	-	-	0/0
568	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 -	1,564.54	420.71	03/2010 03/2017	03/2017	84(O) 0(R)	0/0
569	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	-	- -	-	-	0/0
570	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	1,280.83	1,031.83	- -	-	-	0/0
571	VIRAMGAM-BHILD(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 -	548.01	201.26	- 03/2010	-	-	0/0
572	VIRAMGAM-SAMAKHALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	685.17	206.59	- -	-	-	0/0
573	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	279.40	249.02	- -	-	-	0/0
574	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	2,501.05	84.11	- -	-	-	0/0
575	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	297.85	7.17	- -	-	-	0/0
576	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	348.85	0.34	- -	-	-	0/0

Sector Wise Details

(March 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
577	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	876.00	-	-	-	-	0/0
	Total		163,518.20 -	289,824.76	94,332.06				1/7
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
578	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	363.00	08/2013 -	12/2015	28(O) -	0/0
579	2 LANING OF MUZAFFARPUR - SONBARSA - [N24000174]NHAI,BIHAR	05/2011	511.54 -	511.54	-	11/2013 -	-	-	0/0
580	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI, UTTAR PRADESH	10/2012	250.50 -	250.50	65.26	10/2014 -	03/2015	5(O) -	0/0
581	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	373.47	28.51	07/2014 -	03/2015	8(O) -	0/0
582	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	351.54	-	05/2013 -	-	-	0/0
583	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	1,179.00	11/2013 -	05/2015	18(O) -	0/0
584	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	624.00	333.72	04/2014 -	07/2015	15(O) -	0/0
585	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	356.40	-	07/2014 -	03/2015	8(O) -	0/0
586	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	141.30	01/2014 -	12/2015	23(O) -	0/0
587	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	226.00	282.30	02/2014 -	02/2014	-	0/0
588	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	664.00	776.40	02/2014 -	10/2015	20(O) -	0/0
589	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	408.10	04/2014 -	03/2015	11(O) -	0/0
590	2LANING WITH PS GOPALGANJ-CHAPPRA - [N24000190]NHAI,BIHAR	12/2011	325.00 -	325.00	171.00	05/2014 -	05/2014	-	0/0
591	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT	03/2012	828.00 -	828.00	52.01	09/2014 -	03/2015	6(O) -	0/3
592	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	-	08/2014 -	03/2015	7(O) -	0/0
593	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT	12/2010	1,008.50 -	1,008.50	1,392.00	06/2013 -	08/2014	-	0/3
594	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	39.55	09/2013 -	12/2016	39(O) -	0/0
595	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,GUJARAT	03/2011	785.50 -	785.50	-	08/2013 -	-	-	0/3
596	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	1,266.60	-	09/2016 -	09/2016	0(O) -	0/0
597	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	398.00	462.00	02/2014 -	09/2015	19(O) -	0/0
598	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	998.79	1,610.00	08/2013 -	07/2017	47(O) -	0/0

Sector Wise Details

(March 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
599	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	1,078.84	1,922.00	08/2013 -	08/2016	36(O) -	0/0
600	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	580.43	450.70	08/2013 -	05/2017	45(O) -	0/0
601	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA	10/2013	283.25 -	283.25	-	10/2015 -	10/2015	0(O) -	0/0
602	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	835.60	07/2013 -	12/2015	29(O) -	0/0
603	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	1,396.18	1,934.00	09/2014 -	12/2015	15(O) -	0/0
604	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	465.50	322.70	09/2007 -	06/2015	93(O) -	0/0
605	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	2,125.24	-	12/2015 -	12/2015	0(O) -	0/3
606	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA	02/2010	390.56 -	390.56	631.70	02/2012 -	06/2013	-	0/0
607	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	4,030.00	09/2013 -	12/2015	27(O) -	0/0
608	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	867.00	598.60	02/2015 -	12/2017	34(O) -	0/0
609	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	2,388.00	2,301.00	06/2014 -	11/2015	17(O) -	0/0
610	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,KARNATAKA	12/2010	480.00 -	480.00	-	-	-	-	2/2
611	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	209.00	38.77	01/2013 -	12/2015	35(O) -	0/0
612	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	500.29	633.30	08/2013 -	03/2015	19(O) -	0/0
613	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	237.80	328.60	06/2008 -	09/2015	87(O) -	0/0
614	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	195.00	280.30	06/2008 -	08/2015	86(O) -	0/0
615	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	230.00	251.50	06/2005 -	12/2015	126(O) -	0/0
616	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	309.56	457.70	04/2010 01/2016	01/2016	69(O) 0(R)	0/0
617	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	281.31	180.10	02/2010 -	02/2017	84(O) -	0/0
618	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	901.60	03/2013 -	12/2015	33(O) -	0/0
619	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	353.37	446.20	10/2011 -	06/2016	56(O) -	0/0
620	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	572.30	886.90	10/2011 -	06/2015	44(O) -	0/0
621	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	996.80	05/2013 -	12/2015	31(O) -	0/0
622	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	300.00	176.80	10/2008 -	-	-	0/0
623	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	1,928.22	647.40	04/2015 -	04/2016	12(O) -	0/0
624	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	667.10	05/2010 -	06/2015	61(O) -	0/0

Sector Wise Details

(March 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
625	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	593.00	761.30	07/2013 -	04/2016	33(O) -	0/0
626	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	381.50	06/2013 -	03/2015	21(O) -	0/0
627	DEVIHALLI-HASSAN - [N24000152]NHAI,KARNATAKA	12/2010	453.00 -	453.00	-	- -	-	-	1/1
628	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	200.00	290.00	06/2008 -	03/2015	81(O) -	0/0
629	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	211.80	05/2008 06/2015	06/2015	85(O) 0(R)	0/0
630	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	232.45	317.70	09/2010 -	12/2015	63(O) -	0/0
631	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	1,573.00	-	09/2015 -	09/2015	0(O) -	0/0
632	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	332.94	550.30	09/2008 -	06/2015	81(O) -	0/0
633	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	1,916.79	-	11/2016 -	11/2016	0(O) -	0/0
634	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00 -	1,232.00	87.61	08/2015 -	02/2016	6(O) -	0/0
635	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	682.00	752.70	10/2013 -	11/2015	25(O) -	0/0
636	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	201.66	191.80	09/2008 -	03/2015	78(O) -	0/0
637	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	1,141.00	2,445.00	08/2013 -	06/2015	22(O) -	0/0
638	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	1,509.10	2,686.00	09/2012 -	11/2015	38(O) -	2/3
639	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	198.16	345.80	04/2008 01/2015	03/2015	83(O) 2(R)	0/0
640	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	175.96	290.20	04/2008 04/2015	04/2015	84(O) 0(R)	0/0
641	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	495.40	12/2009 -	04/2015	64(O) -	0/0
642	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	361.00	366.80	02/2009 -	12/2015	82(O) -	0/0
643	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	331.23	242.10	07/2009 -	06/2015	71(O) -	0/0
644	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 -	212.00	127.10	09/2007 -	12/2015	99(O) -	0/0
645	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	478.00	328.70	10/2013 -	12/2015	26(O) -	0/0
646	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	625.07	995.90	01/2013 -	03/2015	26(O) -	0/0
647	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	946.00	737.50	- -	-	-	3/3
648	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	325.00	611.80	05/2013 -	12/2015	31(O) -	0/0

Sector Wise Details

(March 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
649	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	12/2015	32(O) -	0/0
650	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	267.81	699.60	02/2013 -	03/2015	25(O) -	0/0
651	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	792.06	1,983.00	12/2012 -	03/2015	27(O) -	0/0
652	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	1,173.00	07/2013 -	09/2015	26(O) -	0/0
653	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	759.90	01/2014 -	03/2015	14(O) -	0/0
654	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	942.90	07/2013 -	06/2015	23(O) -	0/0
655	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	795.00	1,133.00	05/2012 -	09/2015	40(O) -	0/0
656	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	250.39	285.30	10/2008 -	05/2015	79(O) -	0/0
657	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	726.40	07/2014 -	02/2017	31(O) -	0/0
658	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,KARNATAKA	09/2010	671.00 -	671.00	1,273.00	-	06/2015	-	2/3
659	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	635.90	616.50	07/2012 -	02/2015	-	0/0
660	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	280.13	173.80	11/2008 -	06/2015	79(O) -	0/0
661	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	385.13	159.20	04/2009 -	06/2015	74(O) -	0/0
662	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	167.64	180.30	11/2008 -	06/2015	79(O) -	0/0
663	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	200.00	207.60	04/2009 -	06/2015	74(O) -	0/0
664	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,425.00	06/2013 -	03/2015	21(O) -	0/0
665	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	593.50	03/2013 -	12/2015	33(O) -	0/0
666	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	264.72	315.90	06/2008 -	03/2015	81(O) -	0/0
667	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19 -	484.19	285.50	10/2014 -	03/2015	5(O) -	0/0
668	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	208.00	334.80	04/2008 04/2015	12/2015	92(O) 8(R)	0/0
669	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	276.70	06/2008 04/2015	04/2015	82(O) 0(R)	0/0
670	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	200.00	281.60	06/2008 -	-	-	0/0
671	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	2,159.00	622.70	06/2015 -	06/2016	12(O) -	0/0
672	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	1,655.00	655.20	09/2013 -	11/2016	38(O) -	0/0
673	NH CONNECTIVITY TO ICTT VALLARPADAUEU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	557.00	1,125.00	02/2010 -	01/2015	-	0/0

Sector Wise Details

(March 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
674	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2016	35(O) -	0/0
675	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	929.60	09/2014 -	06/2016	21(O) -	0/0
676	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	11/2015	48(O) -	0/0
677	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00 -	807.00	1,209.43	10/2014 -	10/2014	-	0/0
678	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	942.69	286.80	06/2014 -	12/2015	18(O) -	0/0
679	PATNA-BAKTARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	574.00	991.70	03/2014 -	11/2015	20(O) -	0/0
680	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	632.70	02/2013 -	03/2015	25(O) -	0/0
681	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	940.00	1,601.00	07/2012 -	07/2012	-	0/0
682	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,292.00	03/2013 -	12/2015	33(O) -	0/0
683	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	835.00	476.40	01/2014 -	03/2015	14(O) -	0/0
684	PUNE-SHOLAPUR,PKG1 - [N24000127]NHAI,MAHARASHTRA	11/2009	1,110.00 -	1,110.00	1,826.00	05/2012 -	05/2012	-	0/0
685	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,170.00	07/2015 -	06/2016	11(O) -	0/0
686	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	251.03	385.10	10/2008 -	01/2015	-	0/0
687	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,MULTI STATE	12/2012	1,479.00 -	1,479.00	368.60	06/2015 -	06/2016	12(O) -	0/0
688	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN	03/2012	333.51 -	333.51	152.50	09/2014 -	03/2015	6(O) -	0/0
689	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	650.00	1,178.00	11/2013 -	06/2015	19(O) -	0/0
690	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	805.39	842.20	03/2013 -	12/2015	33(O) -	0/0
691	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	909.00	982.90	05/2014 -	03/2015	10(O) -	0/0
692	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 157.47	154.57	268.50	09/2007 03/2014	03/2015	90(O) 12(R)	0/0
693	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	225.00	191.00	07/2008 -	-	-	0/0
694	SIX LANNING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	1,047.00	295.70	06/2014 -	12/2015	18(O) -	0/0
695	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	535.00	52.18	12/2013 -	03/2015	15(O) -	0/0
696	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,374.00	12/2013 -	05/2015	17(O) -	0/0
697	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	2,188.00	05/2014 -	12/2015	19(O) -	0/0

Sector Wise Details

(March 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
698	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	156.90	08/2012 -	03/2016	43(O) -	0/0
699	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	245.00	491.20	03/2008 03/2015	03/2015	84(O) 0(R)	0/0
700	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	323.00	06/2014 -	12/2015	18(O) -	0/0
701	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	1,693.75	2,762.00	08/2011 -	08/2011	-	2/2
702	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	567.00	1,388.00	11/2013 -	11/2013	-	0/0
703	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	-	10/2013 -	03/2016	29(O) -	0/0
704	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	148.80	05/2013 -	05/2015	24(O) -	0/0
705	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,KARNATAKA	11/2010	680.00 -	680.00	383.20	-	07/2014	-	2/2
706	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,138.00	03/2014 -	04/2017	37(O) -	0/0
707	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI,ANDHRA PRADESH	09/2013	606.00 -	606.00	-	-	-	-	0/0
708	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	193.45	66.11	11/2012 -	12/2016	49(O) -	0/0
709	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	1,287.95	540.40	11/2015 -	03/2017	16(O) -	0/0
710	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	588.40	02/2014 -	08/2016	30(O) -	0/0
711	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI,TELANGANA	04/2014	1,123.17 -	1,123.17	-	-	-	-	0/0
	Total		100,051.44 -	101,992.83	88,192.55				14/28
	<u>SHIPPING AND PORTS</u>								
712	CONST. AND DEV. OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 -	1,460.00	937.28	12/2010 -	-	-	0/0
713	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	600.00	139.80	03/2006 -	-	-	0/0
714	MODIFICATION AND STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST,GUJARAT	06/2010	277.00 -	277.00	0.21	03/2012 -	-	-	0/0
715	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 -	373.22	351.18	04/2009 -	-	-	0/0
716	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	2,427.40	831.23	10/2008 -	-	-	0/0
717	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST,GUJARAT	02/2011	830.00 -	621.53	-	05/2013 -	-	-	0/0

Sector Wise Details

(March 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	Total		5,158.07 -	5,759.15	2,259.70				0/0
	<u>TELECOMMUNICATIONS</u>								
718	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL, ASSAM	06/2007	336.81 -	336.81	195.94	01/2009 -	03/2015	74(O) -	0/0
719	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL, MULTI STATE	10/2009	384.00 -	384.00	54.97	10/2010 08/2015	09/2015	59(O) 1(R)	0/0
720	EXECUTION OF TELECOM NETWORK REQUIREMENT OF DEFENCE FORCES - [N26000065]BSNL, MULTI STATE	05/2006	1,077.00 -	1,077.00	-	03/2009 -	-	-	0/0
721	NETWORK FOR SPECTRUM - [N26000101]DOT, MULTI STATE	03/2012	13,334.00 -	13,334.00	360.00	07/2015 -	07/2015	0(O) -	0/0
	Total		15,131.81 -	15,131.81	610.91				0/0
	<u>URBAN DEVELOPMENT</u>								
722	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD, JHARKHAND	09/2012	171.86 -	171.86	-	03/2016 -	05/2016	2(O) -	0/0
723	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD, WEST BENGAL	01/2009	225.81 -	225.81	17.60	06/2012 -	06/2015	36(O) -	0/0
724	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP, KARNATAKA	05/2006	6,395.00 -	11,609.00	2,267.57	06/2011 -	-	-	3/3
725	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL, KARNATAKA	02/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019	0(O) -	0/0
726	C/O MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB - [N28000070]CPWD, PUNJAB	08/2005	191.24 -	191.24	9.91	08/2007 -	03/2015	91(O) -	0/0
727	C/O MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD, KERALA	01/2010	165.23 -	165.23	-	10/2012 -	09/2013	-	0/0
728	C/O NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD, MAHARASHTRA	12/2012	315.00 -	315.00	88.54	06/2015 -	08/2015	2(O) -	0/0
729	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL, TAMIL NADU	02/2009	14,600.00 -	14,600.00	-	12/2015 -	08/2016	8(O) -	1/24
730	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD, DELHI	07/2012	884.30 -	884.30	103.45	08/2014 -	06/2017	34(O) -	0/0
731	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD, MADHYA PRADESH	12/2012	188.87 -	188.87	24.44	12/2014 -	12/2016	24(O) -	0/0
732	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD, DELHI	05/2009	261.85 -	261.85	131.77	05/2013 -	11/2015	30(O) -	0/0
733	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD, DELHI	05/2012	405.01 -	405.01	-	12/2014 -	04/2016	16(O) -	0/0
734	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD, ODISHA	11/2012	238.43 -	238.43	-	02/2015 -	08/2015	6(O) -	0/0

Sector Wise Details

(March 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
735	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	-	09/2015 -	07/2016	10(O) -	0/0
736	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH	06/2014	157.84 -	157.84	2.31	03/2017 -	03/2017	0(O) -	0/0
737	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	38,585.00	14,321.39	03/2016 -	12/2016	9(O) -	0/0
738	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA - [N28000078]CPWD,BIHAR	11/2006	2,727.89 -	2,727.89	2,637.11	03/2010 -	10/2014	-	0/0
739	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	24.71	11/2014 -	10/2015	11(O) -	0/0
740	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	1,219.21	-	07/2017 -	07/2017	0(O) -	0/0
741	FARIDABAD EXTENSION - [N28000057]DMRCL,DELHI	09/2011	2,494.00 -	2,494.00	1,164.03	09/2014 -	05/2015	8(O) -	0/0
742	KOCHI METRO RAIL PROJECT - [N28000081]KMRL,KERALA	07/2012	5,181.79 -	5,181.79	806.39	07/2017 -	07/2017	0(O) -	0/0
743	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI - [N28000064]CPWD,DELHI	01/2010	162.90 -	162.90	112.06	07/2012 -	06/2014	-	0/0
744	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	12/2015	11(O) -	0/0
745	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	8,680.00	-	03/2018 -	03/2018	0(O) -	0/0
746	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 -	241.33	35.78	11/2014 -	12/2014	-	0/0
747	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI	06/2012	4,264.00 -	4,264.00	421.28	11/2019 -	11/2019	0(O) -	0/7
748	REHABILITATION AND STRENGTHENING OF SEWETRAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI(IN ZONE 2 IN - [N28000082]JnNURM,ANDHRA PRADESH	08/2007	246.90 -	246.90	177.77	-	-	-	0/0
749	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]CPWD,BIHAR	02/2012	171.10 -	171.10	85.60	09/2014 -	09/2014	-	0/0
750	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	332.72	0.11	09/2016 -	12/2016	3(O) -	0/0
751	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	205.00	97.61	03/2012 -	04/2015	37(O) -	0/0
	Total		138,680.82 -	143,894.82	22,529.43				4/34
	Grand Total		1,028,235.95	1,234,208.57	544,538.11				1595/3724


Summary of projects in the Flash Report for the month of March, 2015

Project Implementation - Current Status:

Number of Projects in Previous Month	750
Number of Projects completed/dropped/frozen in Current Month	7
Number of Projects elevated to the status of Major project during the current month	3
Number of Projects Added in Current Month	5
Number of Projects in Current Month	751

Brief Analysis


Project Status with respect to Original Schedule: Out of 751 projects, 3 projects are ahead of schedule, 123 projects are on schedule and 328 projects are delayed. Of the balance, 264 projects do not have fixed dates of commissioning while 33 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

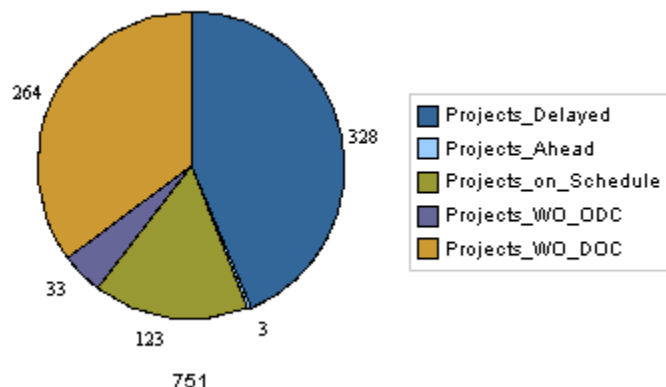

Investment Scenario

Total original cost of implementation of 751 projects when sanctioned, was of the order of Rs. 1028235.95 crore but this was subsequently revised to Rs. 1234208.57 crore implying a cost overrun of 20%. The expenditure incurred on these projects till March, 2015 is Rs. 544538.11 crore, which is 44.1% of the revised cost of the projects.

Figures are in Rs. Crore

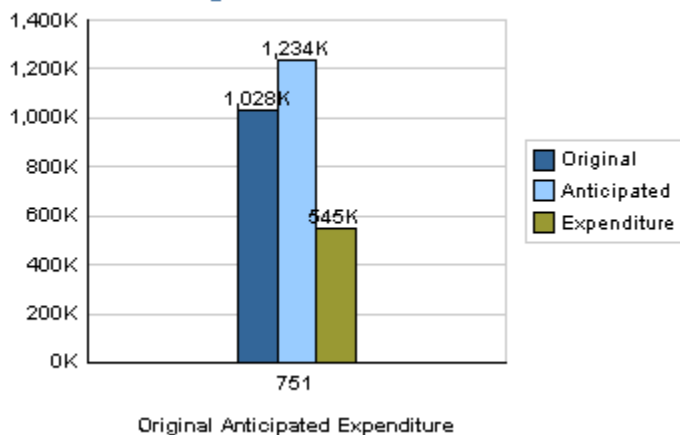

Sector wise current status of projects on the Flash Report


CIVIL AVIATION

Current Status:

Number of Projects	7
Number of Projects Delayed	5
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 7 projects, 5 projects are delayed .1 project do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

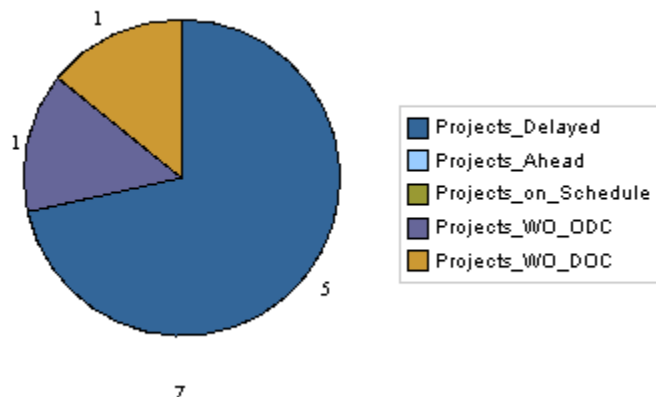

Investment Scenario

Total original cost of implementation of 7 projects when sanctioned, was of the order of Rs. 2599.56 crore but this was subsequently revised to Rs. 2652.48 crore implying a cost overrun of 2%. The expenditure incurred on these projects till March, 2015 is Rs. 1629.3 crore, which is 61.4% of the revised cost of the projects.

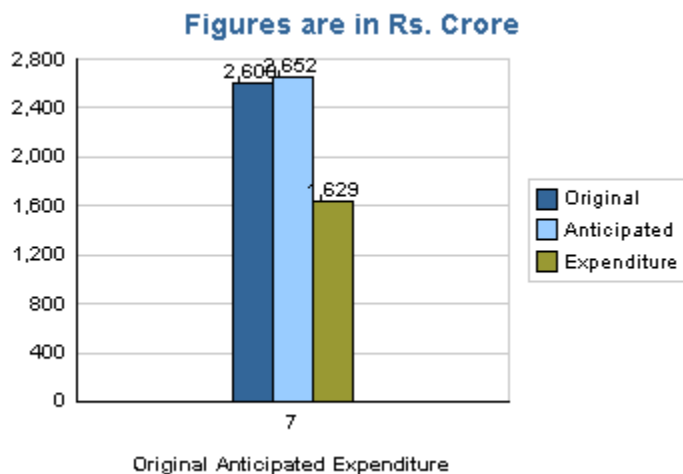

Sector wise current status of projects on the Flash Report

COAL


Current Status:

Number of Projects	73
Number of Projects On Schedule	33
Number of Projects Delayed	37

Number of Projects Without Date Of Commissioning	3
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 73 projects, 33 projects are on schedule and 37 projects are delayed .3 projects do not have fixed dates of commissioning.

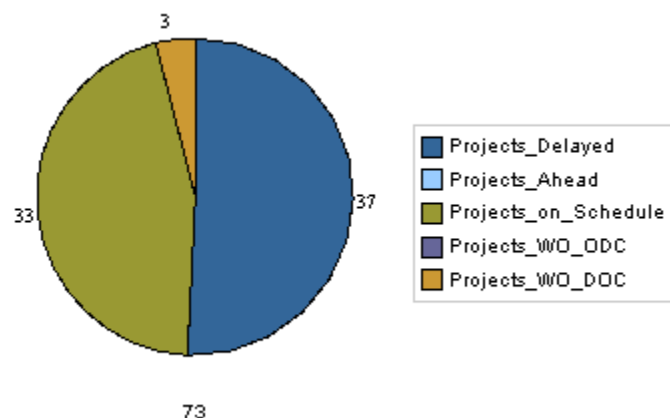

Investment Scenario

Total original cost of implementation of 73 projects when sanctioned, was of the order of Rs. 58516.49 crore but this was subsequently revised to Rs. 55939.62 crore implying a cost overrun of -4.4%. The expenditure incurred on these projects till March, 2015 is Rs. 21079.83 crore, which is 37.7% of the revised cost of the projects.

Figures are in Rs. Crore

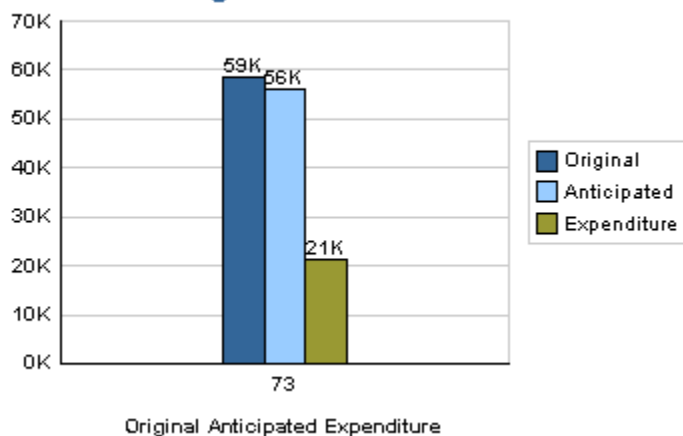

Sector wise current status of projects on the Flash Report


MINES

Current Status:

Number of Projects	1
Number of Projects On Schedule	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 1 project, 1 project are on schedule and

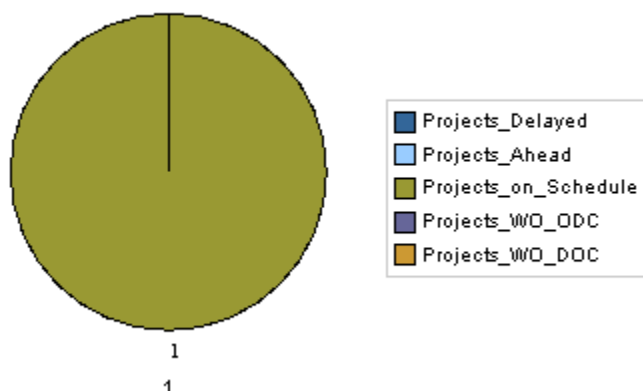

Investment Scenario

Total original cost of implementation of 1 projects when sanctioned, was of the order of Rs. 1856 crore but this was subsequently revised to Rs. 1856 crore implying a cost overrun of 0%. The expenditure incurred on these projects till March, 2015 is Rs. 0 crore, which is 0% of the revised cost of the projects.

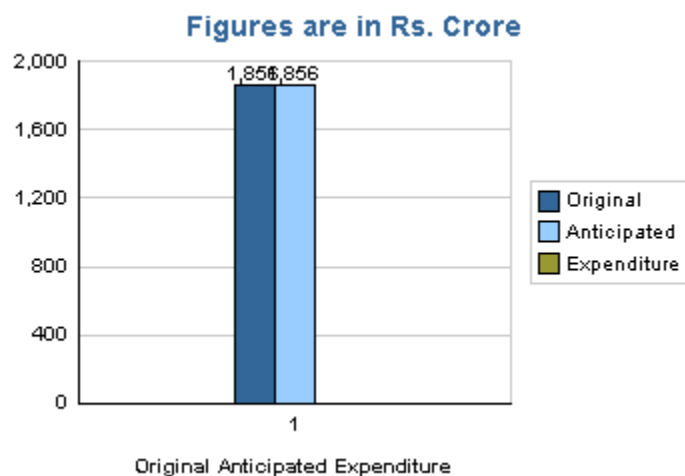

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	72
Number of Projects On Schedule	19
Number of Projects Delayed	43
Number of Projects Ahead	2
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	7


Brief Analysis

Project Status with respect to Original Schedule: Out of 72 projects, 2 projects are ahead of schedule, 19 projects are on schedule and 43 projects are delayed .7 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

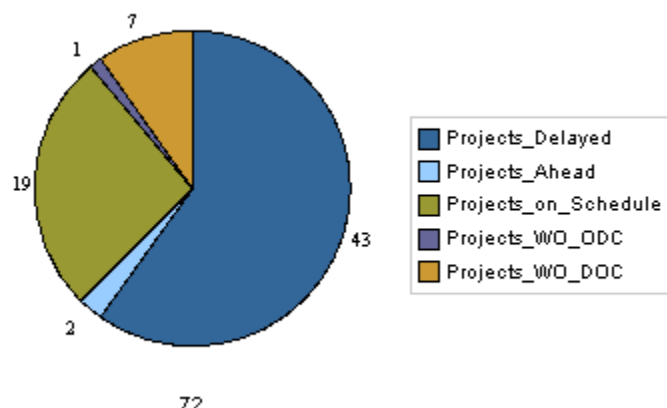

Investment Scenario

Total original cost of implementation of 72 projects when sanctioned, was of the order of Rs. 157335.33 crore but this was subsequently revised to Rs. 174867 crore implying a cost overrun of 11.1%. The expenditure incurred on these projects till March, 2015 is Rs. 74378.94 crore, which is 42.5% of the revised cost of the projects.

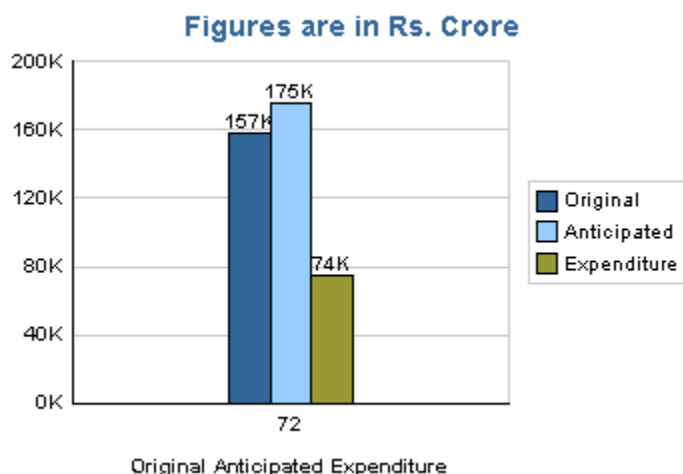

Sector wise current status of projects on the Flash Report


POWER

Current Status:

Number of Projects	105
Number of Projects On Schedule	38
Number of Projects Delayed	63
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	3

Brief Analysis


Project Status with respect to Original Schedule: Out of 105 projects, 1 project are ahead of schedule, 38 projects are on schedule and 63 projects are delayed .3 projects do not have fixed dates of commissioning.

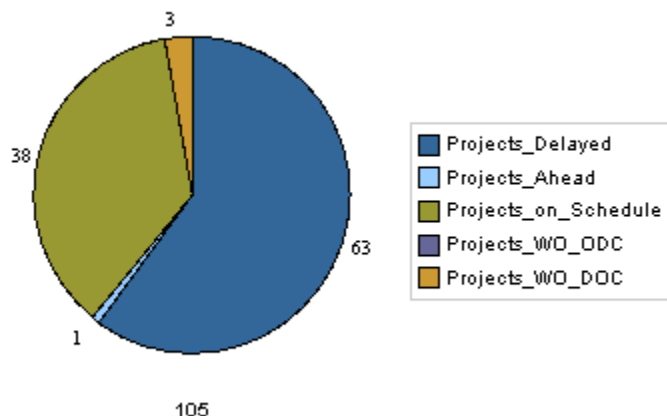

Investment Scenario

Total original cost of implementation of 105 projects when sanctioned, was of the order of Rs. 279607.51 crore but this was subsequently revised to Rs. 316945.69 crore implying a cost overrun of 13.4%. The expenditure incurred on these projects till March, 2015 is Rs. 154014.86 crore, which is 48.6% of the revised cost of the projects.

Figures are in Rs. Crore

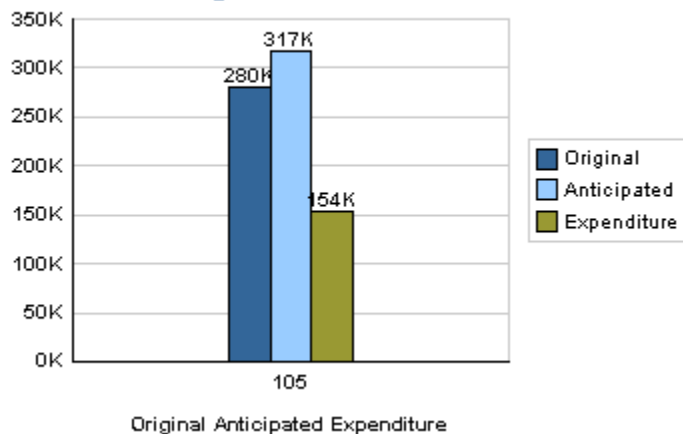

Sector wise current status of projects on the Flash Report

RAILWAYS


Current Status:

Number of Projects	288
Number of Projects On Schedule	11
Number of Projects Delayed	35

Number of Projects Without Original Date of Commissioning	30
Number of Projects Without Date Of Commissioning	212

Brief Analysis


Project Status with respect to Original Schedule: Out of 288 projects, 11 projects are on schedule and 35 projects are delayed .212 projects do not have fixed dates of commissioning.30 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

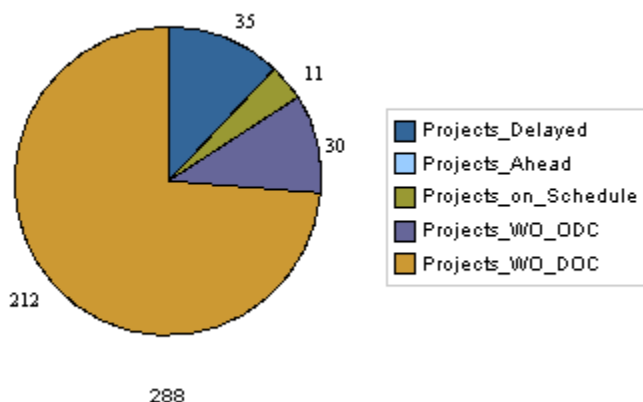

Investment Scenario

Total original cost of implementation of 288 projects when sanctioned, was of the order of Rs. 163518.2 crore but this was subsequently revised to Rs. 289824.76 crore implying a cost overrun of 77.2%. The expenditure incurred on these projects till March, 2015 is Rs. 94332.06 crore, which is 32.5% of the revised cost of the projects.

Figures are in Rs. Crore

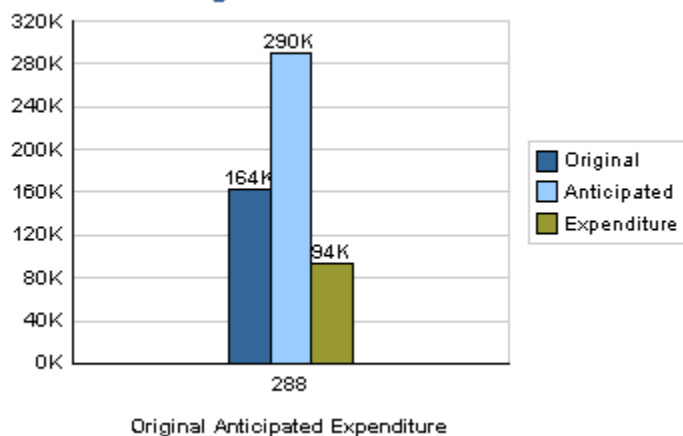

Sector wise current status of projects on the Flash Report

ROAD TRANSPORT AND HIGHWAYS


Current Status:

Number of Projects	134
Number of Projects On Schedule	5
Number of Projects Delayed	104

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	24

Brief Analysis


Project Status with respect to Original Schedule: Out of 134 projects, 5 projects are on schedule and 104 projects are delayed .24 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

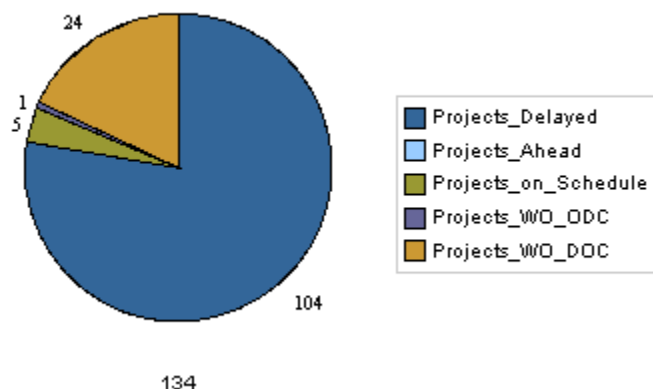

Investment Scenario

Total original cost of implementation of 134 projects when sanctioned, was of the order of Rs. 100051.44 crore but this was subsequently revised to Rs. 101992.83 crore implying a cost overrun of 1.9%. The expenditure incurred on these projects till March, 2015 is Rs. 88192.55 crore, which is 86.5% of the revised cost of the projects.

Figures are in Rs. Crore

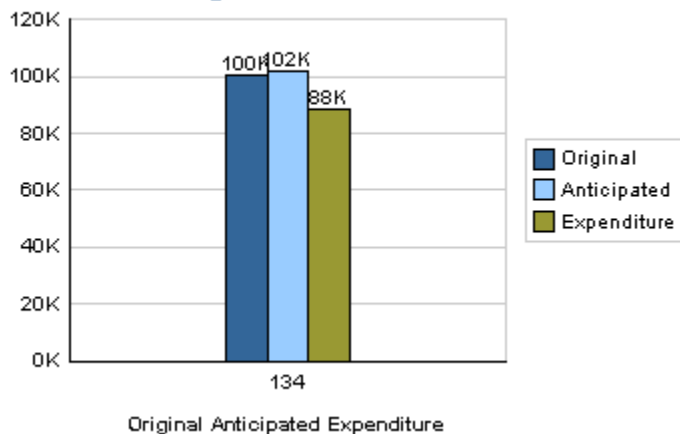

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	4


Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed .

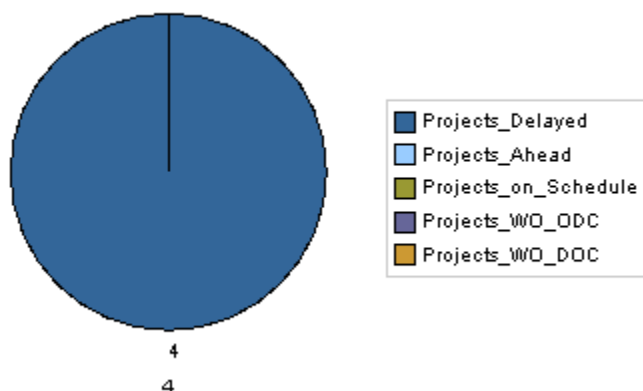

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 40442 crore but this was subsequently revised to Rs. 51918 crore implying a cost overrun of 28.4%. The expenditure incurred on these projects till March, 2015 is Rs. 33554.8 crore, which is 64.6% of the revised cost of the projects.

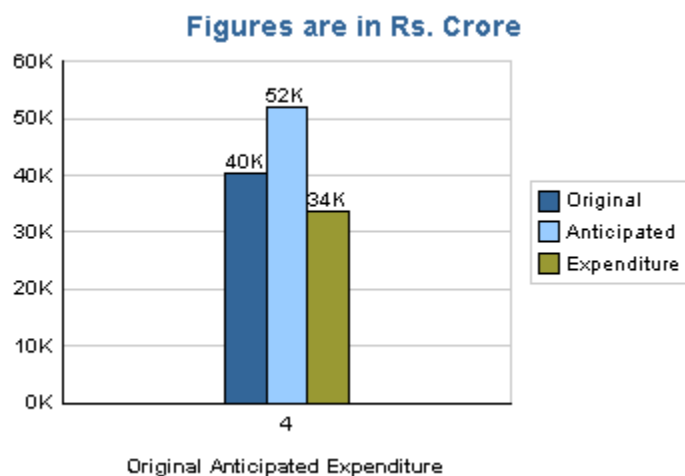

Sector wise current status of projects on the Flash Report

SHIPPING AND PORTS


Current Status:

Number of Projects 6

Number of Projects Without Date Of Commissioning 6

Brief Analysis


Project Status with respect to Original Schedule: Out of 6 projects, 6 projects do not have fixed dates of commissioning.

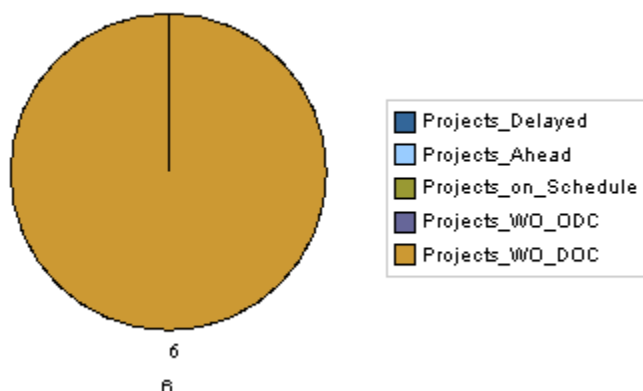

Investment Scenario

Total original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 5158.07 crore but this was subsequently revised to Rs. 5759.15 crore implying a cost overrun of 11.7%. The expenditure incurred on these projects till March, 2015 is Rs. 2259.7 crore, which is 39.2% of the revised cost of the projects.

Figures are in Rs. Crore

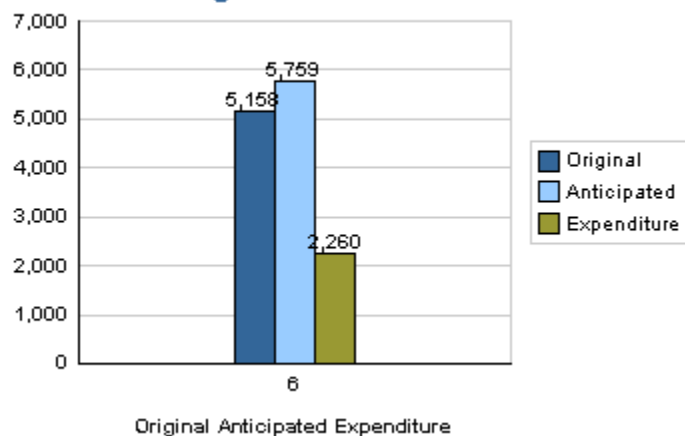

Sector wise current status of projects on the Flash Report


STEEL

Current Status:

Number of Projects	25
Number of Projects On Schedule	8
Number of Projects Delayed	17

Brief Analysis


Project Status with respect to Original Schedule: Out of 25 projects, 8 projects are on schedule and 17 projects are delayed.

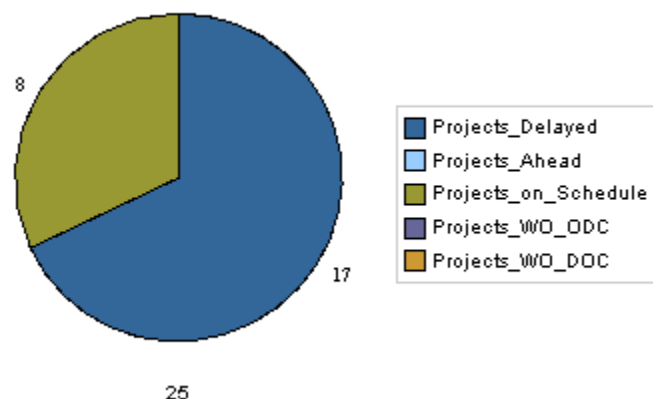

Investment Scenario

Total original cost of implementation of 25 projects when sanctioned, was of the order of Rs. 59680.22 crore but this was subsequently revised to Rs. 63394.62 crore implying a cost overrun of 6.2%. The expenditure incurred on these projects till March, 2015 is Rs. 43484.51 crore, which is 68.6% of the revised cost of the projects.

Figures are in Rs. Crore

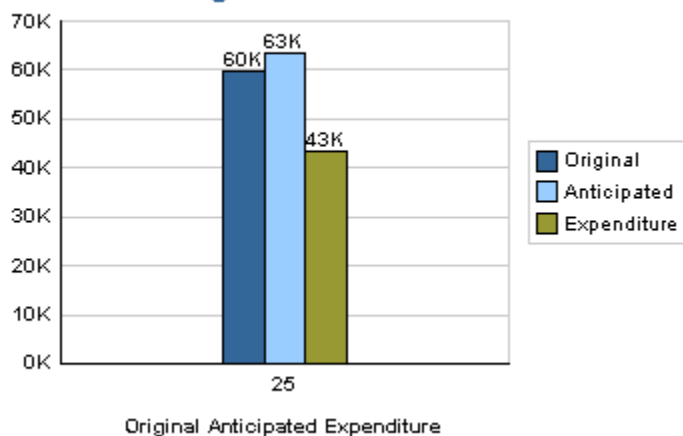

Sector wise current status of projects on the Flash Report

TELECOMMUNICATIONS


Current Status:

Number of Projects	4
Number of Projects On Schedule	1
Number of Projects Delayed	2

Number of Projects Without Date Of Commissioning	1
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 1 project are on schedule and 2 projects are delayed .1 project do not have fixed dates of commissioning.

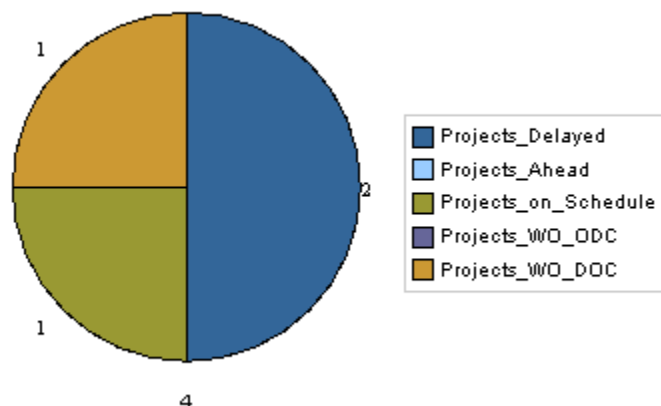

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 15131.81 crore but this was subsequently revised to Rs. 15131.81 crore implying a cost overrun of 0%. The expenditure incurred on these projects till March, 2015 is Rs. 610.91 crore, which is 4% of the revised cost of the projects.

Figures are in Rs. Crore

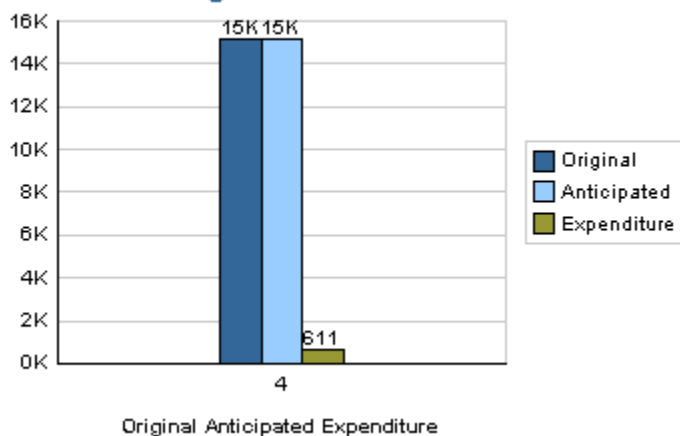

Sector wise current status of projects on the Flash Report

URBAN DEVELOPMENT


Current Status:

Number of Projects	30
Number of Projects On Schedule	6
Number of Projects Delayed	17

Number of Projects Without Date Of Commissioning	7
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 30 projects, 6 projects are on schedule and 17 projects are delayed .7 projects do not have fixed dates of commissioning.

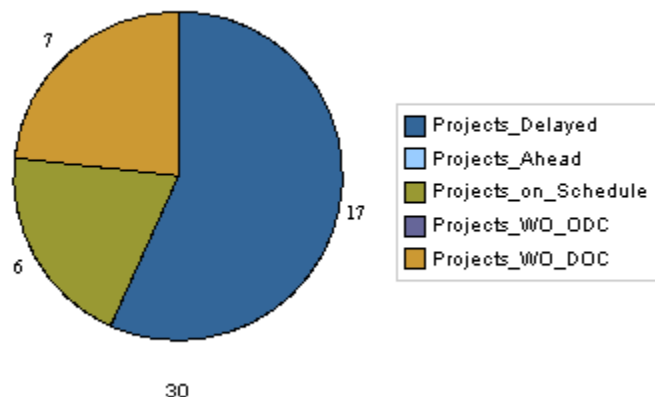

Investment Scenario

Total original cost of implementation of 30 projects when sanctioned, was of the order of Rs. 138680.82 crore but this was subsequently revised to Rs. 143894.82 crore implying a cost overrun of 3.8%. The expenditure incurred on these projects till March, 2015 is Rs. 22529.43 crore, which is 15.7% of the revised cost of the projects.

Figures are in Rs. Crore

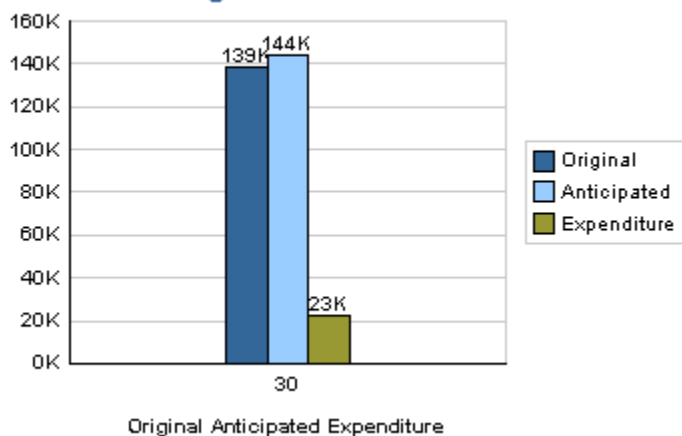

ANNEXURE

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE

(All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	ANDAMAN & NICOBAR ISLANDS	1	314.61	314.61	17.83
2	ANDHRA PRADESH	27	24,854.07	31,076.5	19,133
3	ARUNACHAL PRADESH	3	9,356.22	21,463.83	12,394.81
4	ASSAM	36	23,508.04	41,847.73	33,636.21
5	BIHAR	46	36,458.35	49,774.06	36,460.73
6	CHANDIGARH	1	452	452	410.25
7	CHHATISGARH	28	80,681.93	75,920.08	40,144.35
8	DELHI	11	50,123.12	50,123.12	16,307.84
9	GOA	1	335.61	388.53	295.43
10	GUJARAT	29	36,037.34	36,616.51	18,433.5
11	HARYANA	8	4,259.81	6,230.43	7,163.7
12	HIMACHAL PRADESH	5	11,681.24	19,906.33	11,569.31
13	JAMMU AND KASHMIR	7	21,314.62	40,235.3	17,862.4
14	JHARKHAND	33	36,123.28	36,787.95	14,422.83
15	KARNATAKA	32	64,122.2	79,084.89	19,329.66
16	KERALA	13	24,457.67	28,611.45	10,740.63
17	MADHYA PRADESH	20	24,954.32	26,938.24	8,848.37
18	MAHARASHTRA	46	99,698.94	1,11,372.81	36,446.05
19	MANIPUR	1	727.56	6,570.75	2,787.99
20	MEGHALAYA	3	4,845.02	6,069.9	1,049.99
21	MIZORAM	2	988.06	4,201.96	1,000.05
22	MULTI STATE	184	2,11,384.47	2,39,154.73	83,090.99
23	NAGALAND	2	5,124	7,461.12	10.44
24	ODISHA	41	69,075.25	78,163.29	41,461.58
25	PUNJAB	3	792.5	765.46	120.38
26	RAJASTHAN	25	25,638.72	25,694.2	14,832.46
27	SIKKIM	2	1,648.94	4,499.46	427.13
28	TAMIL NADU	41	67,950.69	90,688.01	49,059.55
29	TELANGANA	21	9,410.62	12,179.13	3,010.89
30	TRIPURA	6	2,966.26	6,617.14	3,255.94
31	UTTAR PRADESH	28	26,759.7	29,864.04	15,834.67
32	UTTARAKHAND	6	9,351.89	12,905.21	4,679.49
33	WEST BENGAL	39	42,838.9	52,229.8	20,299.66
TOTAL		751	10,28,235.95	12,34,208.57	5,44,538.11

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
1	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	COAL	10/2004	2,030.78	3027.59	3,185.95
2	PARBATI HEP (4X200 MW) (NHPC) II	POWER	09/2002	3,919.59	-	4,959.8
3	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	POWER	09/2003	6,285.33	-	7,576.36
4	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	POWER	09/2005	1,061.38	-	1,715.9
5	VIRAMGAM-BHILDI(WR), GC	RAILWAYS	04/1990	155.66	-	201.26
6	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	RAILWAYS	12/1994	124.43	-	712.02
7	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	RAILWAYS	03/1995	2,500	3000	10,658.34
8	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR	RAILWAYS	04/1983	36.8	36.38	255.55
9	CALICUT-MANGALORE (DL) (SR)	RAILWAYS	02/1996	240	-	599.4
10	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR	RAILWAYS	02/1997	295	-	1,060.4
11	KARUR-SALEM(NL), SR	RAILWAYS	02/1997	155.55	-	800.66
12	NANDYAL-YERRAGUNTALA(NL), SCR	RAILWAYS	03/1996	155.74	164.36	755.5
13	KANPUR-KASGANJ-MATHURA(GC), NER	RAILWAYS	03/1997	677.97	1062.36	1,621.4
14	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	RAILWAYS	09/1997	1,500	1000	3,410.06

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
15	MUNEERABAD-MAHABOONAGAR(NL), SCR	RAILWAYS	04/1997	218.24	236.41	309.19
16	RANCHI-LOHARDAGA(GC), SER	RAILWAYS	04/1997	194.07	-	230.67
17	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	RAILWAYS	09/1998	247.66	-	488.76
18	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	RAILWAYS	04/1997	501.69	501.69	802.58
19	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	RAILWAYS	04/1999	108	427.21	436.85
20	KATI HAR - JOGBANI (GC)(NEFR)	RAILWAYS	09/2001	492.98	-	743.74
21	GULBARGA-BIDAR, SCR(NL)	RAILWAYS	02/1998	242.42	369.7	798.87
22	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER)	RAILWAYS	04/1997	863.23	-	888.87
23	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR	RAILWAYS	03/2002	625.3	408.76	835.14
24	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	RAILWAYS	09/1995	100	-	596.66
25	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	RAILWAYS	03/1998	280	-	889.95
26	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	RAILWAYS	04/2000	733	733	1,732.43
27	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	RAILWAYS	03/2000	1,049.69	3385.14	3,538.88
28	GADWAL - RAICHUR (NL), SCR	RAILWAYS	04/1998	92.63	-	301.84

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
29	JIND-SONEPAT (NL), NR	RAILWAYS	01/2004	238.56	-	639.77
30	HARIDASPUR-PARADEEP(NL)	RAILWAYS	04/1996	301.64	-	334.04
31	RAJATGARH-BARANG(LD), ECR	RAILWAYS	04/1999	166.16	-	311.89
32	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	RAILWAYS	04/2003	727.56	727.56	2,787.99
33	KOSI BRIDGE (NL), ECR	RAILWAYS	04/2002	322.95	-	325.92
34	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR	RAILWAYS	04/2002	921	-	1,548.9
35	PATNA GANGA BRIDGE (NL), ECR	RAILWAYS	04/2001	624.47	-	2,339.6
36	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	RAILWAYS	01/2004	915.7	915.7	3,198.3
37	ETAHAWH-MAINPURI (NL), NCR	RAILWAYS	04/1997	120	245.39	249.33
38	CUTTACK - BARANG (LD)	RAILWAYS	04/1995	127.13	-	211.48
39	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RAILWAYS	04/2000	133.41	207	284.12
40	RAICHUR-GUNTAKAL(DL)(SCR)	RAILWAYS	04/2003	136.62	-	284.82
41	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	ROAD TRANSPORT AND HIGHWAYS	12/2003	157.47	157.47	268.5
42	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06	ROAD TRANSPORT AND HIGHWAYS	12/2003	155	-	191.8

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
43	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31C	ROAD TRANSPORT AND HIGHWAYS	12/2003	230	-	251.5
44	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	ROAD TRANSPORT AND HIGHWAYS	12/2003	280	-	366.8
45	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	ROAD TRANSPORT AND HIGHWAYS	12/2003	167.64	-	180.3
46	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	ROAD TRANSPORT AND HIGHWAYS	12/2003	155.04	-	173.8
47	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	ROAD TRANSPORT AND HIGHWAYS	12/2003	200	-	207.6
48	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	195	-	280.3
49	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	237.8	-	328.6
50	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	332.94	-	550.3
51	KOTA BYPASS,RJ-4, NH-76 (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	275	-	285.3
52	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	251.03	-	385.1
53	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	CIVIL AVIATION	01/2009	309.46	-	338.57
54	DEVELOPMENT OF B-193 CLUSTER FIELDS	PETROLEUM	06/2007	3,248.78	5633.44	5,925.4
55	KISHANGANGA HEP (3X110 MW)	POWER	01/2009	3,642.04	-	3,915.36
56	BARH STPP STAGE -II	POWER	02/2008	7,341.04	-	8,594

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
57	TRIPURA GAS BASED POWER PROJECT	POWER	07/2009	421.01	-	898.22
58	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH	POWER	11/2011	2,127.51	-	2,129.33
59	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	RAILWAYS	04/1996	332.92	332.92	488.87
60	BHOPAL BINA 3D LINE DOUBLING	RAILWAYS	09/2007	687.2	-	798.47
61	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	RAILWAYS	09/2007	404.19	-	457.88
62	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	RAILWAYS	09/2006	343.17	-	846.18
63	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	RAILWAYS	12/2006	170	-	417.7
64	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	RAILWAYS	09/2006	200	200	213.72
65	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	RAILWAYS	04/2006	325	-	420.71
66	AGARTALA SABROOM, NL, NEFR	RAILWAYS	04/2008	813.34	813.34	823.83
67	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	RAILWAYS	04/2007	482	-	703.56
68	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	RAILWAYS	04/1999	207.52	-	223.44
69	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	RAILWAYS	04/2006	117.36	196.95	198.83
70	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	RAILWAYS	04/1996	1,676.31	-	4,734.45

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
71	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR	RAILWAYS	04/2013	456	-	557.72
72	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	RAILWAYS	04/2010	739.65	-	794.55
73	SAKRI-HASANPUR ROAD (NL)	RAILWAYS	04/1999	175.69	-	252.75
74	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	RAILWAYS	04/1999	198.68	-	268.56
75	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	RAILWAYS	04/1998	271.24	-	462.69
76	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	RAILWAYS	04/2008	822.39	-	1,031.83
77	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	RAILWAYS	04/1999	895	575	1,005.81
78	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	RAILWAYS	04/2007	247	-	619.87
79	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI	RAILWAYS	04/1999	523.17	380.6	1,040.11
80	PEN ROHA DOUBLING	RAILWAYS	04/2007	98.74	-	227.84
81	PANVEL PEN DOUBLING	RAILWAYS	04/2006	96.16	-	240.21
82	MUNIRABAD (GINGERA) -RAICHUR NL	RAILWAYS	04/2007	179.65	-	339.53
83	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI	RAILWAYS	04/1999	460.94	-	804.2
84	JHARSUGUDA-RENGALI DOUBLING	RAILWAYS	03/2006	201	-	218.67

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
85	NALBARI TO BIJNI (AS-8)	ROAD TRANSPORT AND HIGHWAYS	12/2003	200	-	281.6
86	GUWHATI TO NALBARI (AS-4)	ROAD TRANSPORT AND HIGHWAYS	12/2003	175.96	-	290.2
87	NAGAON TO DHARAMTUL (AS-2)	ROAD TRANSPORT AND HIGHWAYS	12/2003	264.72	-	315.9
88	SONAPUR TO GUWAHTI (AS-3)	ROAD TRANSPORT AND HIGHWAYS	12/2003	245	-	491.2
89	GUWAHATI TO NALBARI (AS-5)	ROAD TRANSPORT AND HIGHWAYS	12/2003	198.16	-	345.8
90	NALBARI TO BIJNI (AS-6)	ROAD TRANSPORT AND HIGHWAYS	12/2003	225	-	276.7
91	NALBARI T BIJNI (AS-7)	ROAD TRANSPORT AND HIGHWAYS	12/2003	208	230	334.8
92	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	ROAD TRANSPORT AND HIGHWAYS	12/2003	160	-	211.8
93	DHARAMTUL TO SONAPUR (AS-19)	ROAD TRANSPORT AND HIGHWAYS	12/2003	200	-	290
94	HARANGAJO TO MAIBANG, NH-54	ROAD TRANSPORT AND HIGHWAYS	12/2003	196	-	242.1
95	BRAHMPUTRA BRIDGE, NH NO-31	ROAD TRANSPORT AND HIGHWAYS	12/2003	217.61	309.56	457.7
96	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	ROAD TRANSPORT AND HIGHWAYS	03/2005	557	-	1,125
97	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	ROAD TRANSPORT AND HIGHWAYS	12/2003	232.45	-	317.7
98	DELHI/ HARYANA BORDER TO ROHTAK	ROAD TRANSPORT AND HIGHWAYS	04/2007	486	-	667.1

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
99	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	ROAD TRANSPORT AND HIGHWAYS	03/2005	940	-	1,601
100	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	ROAD TRANSPORT AND HIGHWAYS	03/2010	1,509.1	-	2,686
101	PUNE-SHOLAPUR, PKG1	ROAD TRANSPORT AND HIGHWAYS	11/2009	1,110	-	1,826
102	KISHANGARH-AJMER-BEAWER	ROAD TRANSPORT AND HIGHWAYS	11/2009	795	-	1,133
103	CHENNAI-TADA(SIX LANE)	ROAD TRANSPORT AND HIGHWAYS	04/2009	353.37	-	446.2
104	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	ROAD TRANSPORT AND HIGHWAYS	02/2009	1,693.75	-	2,762
105	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15)	ROAD TRANSPORT AND HIGHWAYS	05/2009	572.3	-	886.9
106	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	ROAD TRANSPORT AND HIGHWAYS	05/2009	1,108	-	3,466
107	JAIPUR-TONK-DEOLI	ROAD TRANSPORT AND HIGHWAYS	06/2010	792.06	-	1,983
108	TALEGAON-AMRAVATI	ROAD TRANSPORT AND HIGHWAYS	11/2009	567	-	1,388
109	HAZARIBAGH-RANCHI	ROAD TRANSPORT AND HIGHWAYS	08/2010	625.07	-	995.9
110	ARMUR TO KADLOOR YELLAREDDY	ROAD TRANSPORT AND HIGHWAYS	02/2010	390.56	-	631.7
111	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	ROAD TRANSPORT AND HIGHWAYS	09/2010	852	-	901.6
112	KUNDUPUR-SURATHKAL & MANGLORE	ROAD TRANSPORT AND HIGHWAYS	09/2010	671	-	1,273

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
113	DEOLI-KOTA	ROAD TRANSPORT AND HIGHWAYS	01/2011	593	-	761.3
114	PANIPAT-ROHTAK	ROAD TRANSPORT AND HIGHWAYS	04/2011	807	-	1,209.43
115	MURADABAD-BAREILY	ROAD TRANSPORT AND HIGHWAYS	04/2010	1,267	-	2,425
116	INDORE-DEWAS(NH-3)	ROAD TRANSPORT AND HIGHWAYS	11/2010	325	-	611.8
117	4 LANNING OF AHMEDABAD TO GODHARA	ROAD TRANSPORT AND HIGHWAYS	12/2010	1,008.5	-	1,392
118	ROHTAK-BAWAL	ROAD TRANSPORT AND HIGHWAYS	05/2011	650	-	1,178
119	GHAZIABAD-ALIGARH NH-91	ROAD TRANSPORT AND HIGHWAYS	02/2011	1,141	-	2,445
120	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	ROAD TRANSPORT AND HIGHWAYS	09/2011	1,250	-	1,374
121	SAMAIKHIALI - GANDHIDHAM	ROAD TRANSPORT AND HIGHWAYS	09/2010	805.39	-	842.2
122	JORBAT - BARAPANI	ROAD TRANSPORT AND HIGHWAYS	01/2011	536	-	759.9
123	2-LANNING OF SHILONG BYPASS	ROAD TRANSPORT AND HIGHWAYS	02/2011	226	-	282.3
124	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	ROAD TRANSPORT AND HIGHWAYS	11/2011	1,535	-	2,188
125	2-LANNING WITH PS KHAGARIA-PURNEA	ROAD TRANSPORT AND HIGHWAYS	05/2011	664	-	776.4
126	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	ROAD TRANSPORT AND HIGHWAYS	09/2011	574	-	991.7

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
127	2-LANNING WITH PS MOTIHARI-RAXAUL	ROAD TRANSPORT AND HIGHWAYS	10/2011	375.09	-	408.1
128	4-LANNING OF CHAPRA-HAJIPUR	ROAD TRANSPORT AND HIGHWAYS	01/2011	575	-	835.6
129	2 LANNING OF MUZAFFARPUR - SONBARSA	ROAD TRANSPORT AND HIGHWAYS	05/2011	511.54	-	1,179
130	4-LANING OF BARHI-HAZARIBAGH	ROAD TRANSPORT AND HIGHWAYS	02/2012	398	-	462
131	BHUBANESWAR TO PURI	ROAD TRANSPORT AND HIGHWAYS	03/2011	500.29	-	633.3
132	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER	ROAD TRANSPORT AND HIGHWAYS	11/2011	909	-	982.9
133	JAIPUR-REENGUS	ROAD TRANSPORT AND HIGHWAYS	08/2010	267.81	-	699.6
134	BAREILY-SITAPUR (NH-24)	ROAD TRANSPORT AND HIGHWAYS	03/2011	1,046	-	4,030
135	4-LANING OF FARAKA-RAIGANJ	ROAD TRANSPORT AND HIGHWAYS	02/2011	1,078.84	-	1,922
136	4-LANING OF BRAHAMPORE-FARAKA	ROAD TRANSPORT AND HIGHWAYS	02/2011	998.79	-	1,610
137	6-LANING OF DHANKUNI-KHARAGPUR SECTION	ROAD TRANSPORT AND HIGHWAYS	04/2012	1,396.18	-	1,934
138	KRISHNANAGAR-BERHAMPUR	ROAD TRANSPORT AND HIGHWAYS	02/2012	702.16	-	726.4
139	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION	ROAD TRANSPORT AND HIGHWAYS	04/2011	682	-	752.7
140	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	SHIPPING AND PORTS	03/2007	245.67	-	351.18

Details of Projects Without Date of Commissioning

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>CIVIL AVIATION</u>				
1	GAGAN PROJECT - [N04000065]AAI,MULTI STATE	09/2008	626.00	06/2013	-
	Total		626.00		
	<u>COAL</u>				
2	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03	03/2012	-
3	JALLARAM SHAFT PROJECT - [N06000025]SCCL,TELANGANA	09/2007	467.78	03/2013	-
4	MURAI DIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88	04/2014	-
	Total		1,056.69		
	<u>PETROLEUM</u>				
5	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]ONGC,MULTI STATE	03/2010	4,550.40 6,638.94	03/2013 11/2014	02/2015
6	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00	-	-
7	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL,ODISHA	07/2009	199.75	07/2013	-
8	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83	-	-
9	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00	-	-
10	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00	-	-
11	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE	02/2015	890.00	-	-
	Total		10,666.98		
	<u>POWER</u>				
12	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33	09/2010	-
13	SYSTEM STRENGTHENING -XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34	06/2012	-
14	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,ANDHRA PRADESH	03/2012	206.44	06/2014	-
	Total		6,724.11		

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>RAILWAYS</u>				
15	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	07/2008
16	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87 -	- 03/2010	03/2010
17	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	02/2012
18	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 663.01	06/1999 -	07/2012
19	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 03/2012	12/2012
20	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	611.03 -	12/2011 11/2013	11/2013
21	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 -	- -	02/2014
22	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2014
23	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	02/2009 02/2009	08/2014
24	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	03/2009 03/2009	08/2014
25	CUTTACK - BARANG (LD) - [220100326]RVNL,ODISHA	04/1995	127.13 -	- 10/2014	10/2014
26	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 -	03/2009 12/2012	12/2014
27	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	171.02 -	06/2013 -	01/2015
28	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	96.16 -	- -	01/2015
29	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	02/2015 -	02/2015
30	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	- -	-
31	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 -	- 03/2010	-
32	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-
33	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	12/2011 12/2010	-
34	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	- -	-
35	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 -	- -	-
36	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	- -	-
37	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-
38	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-
39	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
40	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222] ECR, JHARKHAND	03/1999	2,957.21 -	07/2005 -	-
41	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232] WCR, MULTI STATE	09/1998	247.66 -	05/2008 -	-
42	JAYANAGAR-DARBHANGA-NARKATIA GANJ (GC), ECR - [220100240] ECR, BIHAR	04/1997	501.69 501.69	03/2012 -	-
43	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252] SR, KERALA	10/1998	550.00 517.70	- -	-
44	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257] ECR, BIHAR	04/1997	162.87 -	- -	-
45	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR - [220100258] NR, MULTI STATE	03/2002	625.30 408.76	06/2007 -	-
46	TIRUCHIRAPPALI-NAGORE-KARAIKKAL (SR)(GC) - [220100262] SR, TAMIL NADU	09/1995	100.00 -	- -	-
47	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR (SR)(GC) - [220100263] SR, MULTI STATE	03/1998	280.00 -	- -	-
48	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265] SCR, ANDHRA PRADESH	12/2001	330.00 -	- -	-
49	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT (MTP) - [220100268] MRTP, WEST BENGAL	03/2000	1,049.69 3,385.14	12/2006 -	-
50	GADWAL - RAICHUR (NL), SCR - [220100270] SCR, MULTI STATE	04/1998	92.63 -	02/2011 02/2011	-
51	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272] ER, WEST BENGAL	04/2000	1,188.91 -	- 12/2009	-
52	DEOGHAR - SULTANGANJ (INL), ER - [220100273] ER, MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-
53	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274] SWR, KARNATAKA	04/1996	138.00 -	- -	-
54	KHURDA ROAD-BOLANGIR (NL) ECR - [220100284] ECR, ODISHA	04/1994	470.21 -	- -	-
55	HARIDASPUR-PARADEEP (NL) - [220100285] RVNL, ODISHA	04/1996	301.64 -	- 09/2009	-
56	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303] ECR, BIHAR	04/2003	528.65 -	- -	-
57	KOSI BRIDGE (NL), ECR - [220100304] ECR, BIHAR	04/2002	322.95 -	03/2012 -	-
58	KODERMA-TILAIYA (NL), ECR - [220100305] ECR, JHARKHAND	04/2002	459.91 -	- -	-
59	DANIAWAN-BIHARSARIF (NL), ECR - [220100311] ECR, BIHAR	04/2001	406.92 -	- -	-
60	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316] NER, BIHAR	04/2003	218.19 -	- -	-
61	HATHUA-BHATNI (N L) (NER) - [220100319] NER, MULTI STATE	04/2005	230.03 -	- -	-
62	TALCHER-BIMALAGARH (NL) (ECOR) - [220100328] ECR, ODISHA	04/2005	810.78 -	- -	-
63	RAICHUR-GUNTAKAL (DL) (SCR) - [220100329] RVNL, ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-
64	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002] ECR, BIHAR	04/1996	332.92 332.92	03/2012 -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
65	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	06/2013 06/2013	-
66	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	378.56 -	- -	-
67	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	261.70 -	02/2006 -	-
68	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-
69	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	03/2010 -	-
70	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	- -	-
71	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE	12/2006	170.00 -	03/2011 -	-
72	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 -	- -	-
73	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 -	- -	-
74	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	1,106.62 -	12/2010 -	-
75	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	03/2014 -	-
76	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 732.06	03/2014 -	-
77	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	-
78	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER,WEST BENGAL	04/2009	533.38 -	12/2011 -	-
79	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER,WEST BENGAL	04/2004	293.74 -	12/2010 -	-
80	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-
81	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	03/2013 -	-
82	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	03/2014 -	-
83	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	-
84	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-
85	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
86	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	-
87	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	-
88	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	- -	-
89	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	- -	-
90	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
91	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	-	-
92	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	-	-
93	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	-	-
94	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	-	-
95	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	-	-
96	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	-	-
97	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 913.48	-	-
98	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT	04/2013	1,266.89 -	-	-
99	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	-	-
100	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	-	-
101	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	-	-
102	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	-	-
103	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	-	-
104	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	-	-
105	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	-	-
106	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	-	-
107	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	-	-
108	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	-	-
109	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	-	-
110	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	-	-
111	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	-	-
112	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	-	-
113	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	-	-
114	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	-	-
115	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	-	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
116	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-
117	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-
118	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-
119	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-
120	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-
121	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-
122	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-
123	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-
124	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-
125	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-
126	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
127	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-
128	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-
129	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-
130	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	- -	-
131	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-
132	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
133	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-
134	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-
135	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	- -	-
136	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-
137	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
138	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	- -	-
139	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
140	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
141	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-
142	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-
143	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-
144	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-
145	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	- -	-
146	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-
147	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-
148	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-
149	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-
150	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-
151	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-
152	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-
153	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-
154	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-
155	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-
156	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-
157	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-
158	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	- -	-
159	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-
160	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-
161	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-
162	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-
163	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-
164	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
165	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-
166	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-
167	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-
168	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-
169	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	- -	-
170	SANTOSHPUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-
171	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-
172	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-
173	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-
174	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-
175	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	- -	-
176	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-
177	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE	04/2013	723.00 -	- -	-
178	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 -	- -	-
179	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE	04/2008	184.26 -	- -	-
180	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-
181	GUDUR-DURGARAJPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-
182	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-
183	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-
184	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-
185	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-
186	DELHI-SOHNANUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-
187	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-
188	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
189	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-
190	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	-
191	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-
192	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-
193	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	- -	-
194	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-
195	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-
196	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
197	MUDKHED-PARBHANI - [N22000283]SCR,MAHARASHTRA	04/2011	390.60 -	- -	-
198	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	- -	-
199	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49 -	- -	-
200	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	- -	-
201	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
202	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-
203	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-
204	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-
205	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-
206	UNCHAHAH-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-
207	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-
208	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-
209	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	- -	-
210	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-
211	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	- -	-
212	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	-
213	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-
214	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
215	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	01/1999 -	-
216	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 -	-
217	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-
218	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	01/1999 -	-
219	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-
220	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 -	- -	-
221	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 -	- -	-
222	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	- -	-
223	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	- -	-
224	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-
225	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR,TAMIL NADU	04/2011	190.10 -	- -	-
226	HOSADURGA - CHICKJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA	04/2010	203.40 -	- -	-
	Total		102,529.83 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
227	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	08/2011 -	08/2011
228	PUNE-SHOLAPUR,PKG1 - [N24000127]NHAI,MAHARASHTRA	11/2009	1,110.00 -	05/2012 -	05/2012
229	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	07/2012 -	07/2012
230	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA	02/2010	390.56 -	02/2012 -	06/2013
231	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	11/2013
232	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	02/2014 -	02/2014
233	2LANING WITH PS GOPALGANJ-CHAPPRA - [N24000190]NHAI,BIHAR	12/2011	325.00 -	05/2014 -	05/2014
234	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,KARNATAKA	11/2010	680.00 -	- -	07/2014
235	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT	12/2010	1,008.50 -	06/2013 -	08/2014
236	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00 -	10/2014 -	10/2014
237	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	10/2008 -	01/2015
238	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	02/2010 -	01/2015

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
239	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	07/2012 -	02/2015
240	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	10/2008 -	-
241	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	07/2008 -	-
242	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-
243	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	- -	-
244	DEVIHALLI-HASSAN - [N24000152]NHAI,KARNATAKA	12/2010	453.00 -	- -	-
245	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,KARNATAKA	12/2010	480.00 -	- -	-
246	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	-
247	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,GUJARAT	03/2011	785.50 -	08/2013 -	-
248	2 LANING OF MUZAFFARPUR - SONBARSA - [N24000174]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	-
249	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI,ANDHRA PRADESH	09/2013	606.00 -	- -	-
250	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI,TELANGANA	04/2014	1,123.17 -	- -	-
	Total		15,173.49 -		
	<u>SHIPPING AND PORTS</u>				
251	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-
252	CONST. AND DEV. OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 -	12/2010 -	-
253	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	03/2006 -	-
254	MODIFICATION AND STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST,GUJARAT	06/2010	277.00 -	03/2012 -	-
255	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 -	04/2009 -	-
256	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST,GUJARAT	02/2011	830.00 -	05/2013 -	-
	Total		5,158.07 -		
	<u>TELECOMMUNICATIONS</u>				
257	EXECUTION OF TELECOM NETWORK REQUIREMENT OF DEFENCE FORCES - [N26000065]BSNL,MULTI STATE	05/2006	1,077.00 -	03/2009 -	-
	Total		1,077.00 -		
	<u>URBAN DEVELOPMENT</u>				

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
258	C/O MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	10/2012 -	09/2013
259	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI - [N28000064]CPWD,DELHI	01/2010	162.90 -	07/2012 -	06/2014
260	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]CPWD,BIHAR	02/2012	171.10 -	09/2014 -	09/2014
261	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA - [N28000078]CPWD,BIHAR	11/2006	2,727.89 -	03/2010 -	10/2014
262	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 -	11/2014 -	12/2014
263	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA	05/2006	6,395.00 -	06/2011 -	-
264	REHABILITATION AND STRENGTHENING OF SEWEWAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI(IN ZONE 2 IN - [N28000082]JnNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-
	Total		10,110.35 -		
	Grand Total		153,122.52		

Details of Projects without Original Date of Commissioning

(March 2015)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>CIVIL AVIATION</u>								
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	314.61	17.83	- -	09/2018	-	0/0
	Total		314.61 -	314.61	17.83				0/0
	<u>PETROLEUM</u>								
2	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL, MULTI STATE	01/2015	690.00 -	690.00	-	- -	07/2018	-	0/31
	Total		690.00 -	690.00	.00				0/31
	<u>RAILWAYS</u>								
3	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER, UTTAR PRADESH	03/1997	677.97 1,062.36	1,651.54	1,621.40	- -	03/2015	-	0/0
4	MUNEERABAD-MAHABOONAGAR(NL),SCR - [220100205]SCR, MULTI STATE	04/1997	218.24 236.41	645.00	309.19	- -	03/2015	-	0/0
5	GULBARGA-BIDAR, SCR(NL) - [220100254]SCR, KARNATAKA	02/1998	242.42 369.70	844.00	798.87	- 05/2009	03/2015	70(R1)	0/0
6	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]NFR, ASSAM	01/2004	915.70 915.70	3,700.00	3,198.30	- -	03/2015	-	0/0
7	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR, TAMIL NADU	09/2006	343.17 -	914.98	846.18	- -	03/2015	-	0/0
8	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONG WITH ELECTRIF - [N22000202]SR, TAMIL NADU	04/2007	247.00 -	951.24	619.87	- -	03/2015	-	0/0
9	PEN ROHA DOUBLING - [N22000254]CR, MULTI STATE	04/2007	98.74 -	203.00	227.84	- -	03/2015	-	0/0
10	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER, UTTAR PRADESH	04/1997	863.23 -	1,072.51	888.87	- -	06/2015	-	0/0
11	KAPTANGANJ-THAWA-SIWAN-CHHAPRA GC (NER) - [220100256]NER, MULTI STATE	04/1999	744.71 -	744.71	576.86	- -	03/2016	-	0/1
12	RAMGANJ-MUNDI-BHOPAL (NL), WCR - [220100314]WCR, MADHYA PRADESH	04/2001	470.92 727.13	1,225.90	257.59	- -	03/2017	-	0/0
13	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, MADHYA PRADESH	04/2005	383.79 663.67	1,101.16	194.91	- -	03/2017	-	0/0

[illegible]

(March 2015)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Antici Pated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
33	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,KARNATAKA	09/2010	671.00 -	671.00	1,273.00	- -	06/2015	-	2/3
	Total		671.00 -	671.00	1,273.00				2/3
	Grand Total		17,918.30	33,828.90	13,132.77				2/35

Details of On Schedule Projects w.r.t. Original Schedule

(March 2015)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Antici Pated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
1	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008	8/2013	7,612.33 -	1,188.31	756.61	03/2023 03/2023	03/2023
2	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010	12/2009	1,352.04 -	1,143.54	778.29	03/2016 -	03/2016
3	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034	12/2007	490.10 -	490.10	186.68	03/2017 -	03/2017
4	PELMA OCP(15.00MTY) - [N06000045	11/2014	1,624.59 -	1,624.59	0.46	03/2023 03/2023	03/2023
5	BATURA OCP (2.0 MTY) - [N06000049	9/2008	203.82 -	203.82	-	03/2015 -	03/2015
6	PENGANGA OCP(REVISED) - [N06000066	9/2014	441.82 -	441.82	98.00	03/2020 -	03/2020
7	RKP OCP PHASE-I - [N06000079	3/2010	209.78 -	209.78	74.96	03/2015 -	03/2015
8	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082	11/2009	150.59 -	198.59	94.90	03/2016 -	03/2016
9	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087	12/2009	510.85 -	510.85	223.68	03/2016 -	03/2016
10	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091	6/2011	1,131.28 -	1,131.28	77.88	03/2018 -	03/2018
11	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093	7/2011	162.76 -	162.76	2.48	03/2015 -	03/2015
12	MOONIDIH XV SEAM UG - [N06000098	8/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015
13	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099	4/2012	258.56 -	258.56	74.44	03/2016 -	03/2016
14	RFR OF MANUGURU OC PROJECT - [N06000102	11/2012	430.45 -	430.14	69.91	03/2016 -	03/2016
15	AMRAPALI OC(12MTY) - [N06000103	2/2012	858.11 -	858.11	101.90	03/2020 -	03/2020
16	CHHAL OC SEAM -III (6.00 MTY) - [N06000104	12/2013	610.63 -	610.33	-	03/2022 -	03/2022
17	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106	2/2014	555.52 -	555.52	6.84	03/2021 -	03/2021
18	KAPURIA UG(PSLW) - [N06000108	8/2011	988.35 -	988.35	6.84	04/2017 -	04/2017
19	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109	8/2012	1,055.05 -	1,055.05	148.67	03/2018 -	03/2018
20	BIJARI OC RCE (1.50 MTY) - [N06000111	5/2014	164.49 -	164.49	22.10	03/2020 -	03/2020
21	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112	5/2014	479.15 -	479.15	6.34	03/2019 -	03/2019
22	SIARMAL OCP (40.00MTY) - [N06000113	5/2014	3,756.36 -	3,756.36	0.65	03/2026 -	03/2026

(March 2015)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
23	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114	5/2014	337.66 -	337.66	-	03/2019 -	03/2019
24	KULDA EXPN OC. (5.00 MTY) - [N06000115	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
25	GARJANBAHAL OCP - [N06000117	11/2014	1,375.38 -	1,375.38	2.49	03/2021 -	03/2021
26	DINESH OCP - [N06000118	11/2014	611.16 -	611.16	6.02	03/2020 -	03/2020
27	MAKARDHOKRA I OC - [N06000119	9/2014	266.23 -	266.23	61.70	03/2021 -	03/2021
28	GOKUL - [N06000120	11/2014	267.67 -	267.67	68.35	03/2018 -	03/2018
29	BHANEAGAON OC - [N06000121	2/2015	187.94 -	187.94	20.59	03/2023 -	03/2023
30	AMRITDHARA OC PROJECT - [N06000122	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
31	AMERA OC RCE - [N06000123	2/2015	335.97 -	335.97	30.30	03/2018 -	03/2018
32	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124	12/2014	357.80 -	357.80	106.44	03/2021 -	03/2021
33	KANCHAN OC EXPANSION - [N06000125	12/2014	371.04 -	371.04	30.24	03/2021 -	03/2021
	Total		29,158.38 -	22,573.25	3,057.76		
	<u>FERTILISERS</u>						
34	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009	10/2014	197.79 -	197.79	12.09	11/2016 -	11/2016
	Total		197.79 -	197.79	12.09		
	<u>MINES</u>						
35	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007	9/2011	1,856.00 -	1,856.00	-	09/2017 -	09/2017
	Total		1,856.00 -	1,856.00	.00		
	<u>PETROLEUM</u>						
36	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132	3/2012	5,608.40 -	5,608.40	3,576.16	05/2015 -	05/2015
37	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159	9/2011	202.25 -	160.16	39.42	07/2016 -	07/2016
38	SURAT PARADIP PIPELINE PROJECT - [N16000163	10/2012	10,281.00 -	10,281.00	1.36	04/2015 -	04/2015
39	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172	5/2013	4,124.35 -	4,124.35	75.24	04/2016 04/2016	04/2016
40	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177	4/2013	480.00 -	480.00	23.70	02/2016 -	02/2016

(March 2015)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
41	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]	2/2014	163.88 -	163.88	14.86	07/2016 -	07/2016
42	TWENTY NOS. FEEDER GAS LINES - [N16000192]	3/2009	228.64 -	214.19	122.59	12/2016 -	12/2016
43	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]	12/2011	160.00 -	160.00	2.32	02/2016 -	02/2016
44	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]	7/2014	419.04 -	419.04	27.85	01/2017 -	01/2017
45	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	6/2014	5,706.47 -	5,813.25	300.65	05/2017 05/2017	05/2017
46	RESID UPGRADATION PROJECT - [N16000184]	2/2011	3,110.36 -	3,110.36	508.71	11/2015 -	11/2015
47	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]	3/2014	2,476.82 -	2,476.82	-	12/2018 -	12/2018
48	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00 -	3,150.00	96.36	09/2017 -	09/2017
49	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]	3/2014	3,076.00 -	3,076.00	91.65	09/2017 -	09/2017
50	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	7/2011	352.56 -	450.55	10.60	03/2017 -	03/2017
51	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]	3/2013	1,138.50 -	686.58	-	04/2015 04/2015	04/2015
52	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]	2/2011	913.00 -	913.00	379.89	08/2015 -	08/2015
53	REWARI KANPUR PIPELINE PROJECT - [N16000145]	2/2012	1,210.64 -	1,446.34	982.15	11/2015 -	11/2015
54	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	3/2012	14,225.00 -	16,504.00	5,828.23	05/2016 -	05/2016
	Total		57,026.91 -	59,237.92	12,081.74		
	POWER						
55	VINDHYACHAL STPP STAGE-V - [N18000134]	5/2012	3,180.40 -	3,180.40	1,740.00	08/2015 -	08/2015
56	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]	9/2013	1,575.30 -	1,575.30	214.60	05/2016 -	05/2016
57	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]	1/2014	374.63 -	374.63	-	04/2016 -	04/2016
58	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]	3/2015	1,394.52 -	1,394.52	-	06/2017 -	06/2017
59	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]	3/2015	550.06 -	550.06	-	04/2018 -	04/2018
60	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]	3/2015	1,071.24 -	1,071.24	-	10/2017 -	10/2017
61	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]	3/2015	197.40 -	197.40	-	04/2018 -	04/2018
62	WARDHA-HYDERABAD 765 KV LINK - [N18000183]	1/2015	3,662.02 -	3,662.02	-	05/2018 -	05/2018

(March 2015)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
63	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	1/2015	203.28 -	203.28	-	07/2017 -	07/2017
64	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]	1/2015	871.62 -	871.62	-	10/2017 -	10/2017
65	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]	1/2015	268.80 -	268.80	-	03/2018 -	03/2018
66	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]	12/2014	6,517.36 -	6,517.36	-	04/2018 -	04/2018
67	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.84	109.00	09/2019 -	09/2019
68	TRANS. SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]	6/2014	400.47 -	400.47	-	04/2017 -	04/2017
69	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]	2/2014	378.71 -	378.71	34.00	10/2016 -	10/2016
70	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 -	522.29	-	11/2016 -	11/2016
71	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]	5/2014	303.07 -	303.07	1.00	07/2016 -	07/2016
72	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]	5/2014	829.98 -	829.98	-	08/2016 -	08/2016
73	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]	2/2014	167.40 -	167.40	3.00	12/2015 -	12/2015
74	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]	2/2014	243.53 -	243.53	44.00	08/2016 -	08/2016
75	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	2/2014	908.08 -	908.08	20.00	06/2016 -	06/2016
76	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]	2/2014	539.82 -	539.82	14.00	06/2016 -	06/2016
77	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58 -	14,366.58	2,056.00	02/2019 -	02/2019
78	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	12,532.44	1,408.00	08/2018 -	08/2018
79	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	578.00	03/2019 -	03/2019
80	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]	11/2014	972.42 -	972.42	-	11/2017 -	11/2017
81	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]	10/2014	8,112.12 -	8,112.12	-	04/2020 -	04/2020
82	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	2/2014	196.58 -	196.58	-	02/2016 -	02/2016
83	TRANS. SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]	8/2014	188.75 -	188.75	-	02/2017 -	02/2017
84	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]	8/2014	288.49 -	288.49	-	02/2017 -	02/2017
85	TRANS.SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	442.00	03/2018 -	03/2018
86	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,364.52	135.34	04/2016 -	04/2016

(March 2015)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
87	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]	9/2013	680.69 -	680.69	164.49	03/2016 -	03/2016
88	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	147.00	08/2017 -	08/2017
89	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	3/2013	514.20 -	514.20	102.00	06/2015 -	06/2015
90	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	11,638.55	2,772.00	09/2017 -	09/2017
91	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]	3/2013	2,514.88 -	2,514.88	480.65	12/2015 -	12/2015
92	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	11,846.00	3,718.00	06/2017 -	06/2017
	Total		106,625.39 -	106,625.39	14,183.08		
	<u>RAILWAYS</u>						
93	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	4/2010	3,951.98 -	3,951.98	584.90	03/2016 -	03/2016
94	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	4/2012	148.77 -	209.00	2.64	12/2016 -	12/2016
95	DELANG-PURI DOUBLING - [N22000320]	3/2011	165.16 -	234.71	137.01	03/2015 -	03/2015
96	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	4/2010	423.66 -	423.66	263.01	03/2017 -	03/2017
97	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	3/2013	4,874.58 -	4,874.58	2,371.00	03/2016 -	03/2016
98	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	1,176.09 -	3,845.60	2.33	02/2020 -	02/2020
99	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]	4/2010	622.41 -	2,030.50	3.61	02/2019 -	02/2019
100	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	4/2011	299.60 -	299.60	1.10	03/2017 -	03/2017
101	PLASSEY-JIAGANJ DOUBLING - [N22000220]	4/2011	248.07 -	248.07	29.10	03/2015 -	03/2015
102	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]	4/2008	829.74 -	829.74	93.08	03/2015 -	03/2015
103	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	4/2010	2,913.51 -	2,619.02	525.84	03/2016 -	03/2016
	Total		15,653.57 -	19,566.46	4,013.62		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
104	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	-	09/2015 -	09/2015
105	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	4/2014	1,266.60 -	1,266.60	-	09/2016 -	09/2016

(March 2015)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
106	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]	11/2013	1,916.79 -	1,916.79	-	11/2016 -	11/2016
107	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	-	12/2015 -	12/2015
108	4-LANING OF ROHATAK JIND (LENGTH 45 KM) - [N24000231]	10/2013	283.25 -	283.25	-	10/2015 -	10/2015
	Total		7,164.88 -	7,164.88	.00		
	<u>STEEL</u>						
109	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]	11/2012	313.05 -	313.05	205.93	06/2015 -	06/2015
110	REBUILDING OF COB-7 AT BSL - [N12000083]	10/2013	245.67 -	245.67	32.31	05/2016 -	05/2016
111	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]	6/2014	708.91 -	708.91	99.30	04/2016 -	04/2016
112	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT [N12000085]	4/2014	188.93 -	188.93	16.95	04/2015 -	04/2015
113	3RD CONVERTER AND 4TH CASTER - [N12000088]	7/2011	974.76 -	974.76	69.15	07/2016 -	07/2016
114	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	23.52	10/2016 -	10/2016
115	TURBO BLOWER - 5 - [N12000092]	12/2009	280.00 -	280.00	2.00	09/2016 -	09/2016
116	ALTERNATE GAS NETWORK AT BSL - [N12000093]	3/2015	255.19 -	255.19	-	03/2018 -	03/2018
	Total		3,309.51 -	3,454.91	449.16		
	<u>TELECOMMUNICATIONS</u>						
117	NETWORK FOR SPECTRUM - [N26000101]	3/2012	13,334.00 -	13,334.00	360.00	07/2015 -	07/2015
	Total		13,334.00 -	13,334.00	360.00		
	<u>URBAN DEVELOPMENT</u>						
118	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]	2/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019
119	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,219.21	-	07/2017 -	07/2017
120	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]	6/2014	157.84 -	157.84	2.31	03/2017 -	03/2017
121	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,264.00	421.28	11/2019 -	11/2019
122	KOCHI METRO RAIL PROJECT - [N28000081]	7/2012	5,181.79 -	5,181.79	806.39	07/2017 -	07/2017
123	NAGPUR METRO RAIL - [N28000085]	8/2014	8,680.00 -	8,680.00	-	03/2018 -	03/2018

(March 2015)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		45,907.98	45,907.98	1,229.98		
	Grand Total		280,234.41	279,918.58	35,387.43		

Details of Projects Ahead of Schedule w.r.t. Original Schedule

(March 2015)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>PETROLEUM</u>						
1	KOTA JOBNER PIPELINE PROJECT - [N16000170]	4/2011	276.26 -	276.27	241.63	12/2015 -	03/2015
2	MARKETING TOP AT KORBA - [N16000186]	1/2011	141.86 -	232.00	126.07	09/2016 -	12/2015
	Total		418.12 -	508.27	367.70		
	<u>POWER</u>						
3	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154]	10/2013	1,315.90 -	1,315.90	365.47	10/2016 -	03/2016
	Total		1,315.90 -	1,315.90	365.47		
	Grand Total		1,734.02	1,824.17	733.17		

Details of Delayed Projects w.r.t. Original and Revised Schedule

(March 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL, TAMIL NADU	12/2001	13,171.00 22,462.00	22,462.00	18,271.00	12/2008 10/2013	07/2015	79	70.54	The work progress at Kudankulam site got badly affected since mid September 2011 due to local protest/ agitation. Working situation has been normalised on March 19, 2012. On-going work is also affected due to slippage of commitments by Atomstroyexport (ASE), Russia.
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI, TAMIL NADU	09/2003	3,492.00 5,677.00	5,677.00	4,933.80	09/2010 09/2016	09/2016	72	62.57	Delay in delivery of certain critical items on account of longer than expected time taken for rigorous testing and qualification.
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 -	11,459.00	6,297.00	12/2015 -	10/2017	22	0	Delay in supply of equipments from M/s L&T and BHEL
4	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 -	12,320.00	4,053.00	12/2016 -	05/2018	17	0	Delay in supply of equipments from M/s L&T and BHEL
	Total		40,442.00 -	51,918.00	33,554.80					
	<u>CIVIL AVIATION</u>									
5	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI, GOA	05/2010	335.61 -	388.53	295.43	05/2012 -	03/2015	34	15.77	
6	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]AAI, CHANDIGARH	02/2011	452.00 489.00	452.00	410.25	03/2015 -	04/2015	1	0	
7	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI, MULTI STATE	02/2010	344.28 -	344.28	52.48	03/2014 -	04/2015	13	0	
8	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI, MULTI STATE	10/2012	217.60 -	217.60	0.04	03/2015 -	09/2015	6	0	
9	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI, SIKKIM	01/2009	309.46 -	309.46	338.57	01/2011 -	06/2016	65	0	

(March 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	Total		1,658.95	1,711.87	1,096.77					
	<u>COAL</u>									
10	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98	210.98	186.69	03/2013	03/2015	24	0	i)Rehabilitations &Resettlement Problems ii)Law & Order iii) Environmental Clearance
11	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,TAMIL NADU	10/2004	2,030.78 3,027.59	3,477.21	3,185.95	06/2009 03/2013	04/2015	70	71.23	i) Delay in acceptance testing and handover ii) Inadequate mobilization by the contractor
12	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	6,115.69	03/2012 05/2014	04/2015	37	34.63	Inadequate mobilization of resources by the contractor M/s BHEL and slow progress of civil,structural fabrication and erection.
13	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]NLC,TAMIL NADU	04/2012	364.75	364.75	128.27	10/2014	06/2015	8	0	i)Delay in acquisition of private lands ii)Delay in civil works iii)Delay in equipment erection iv)Delay in acquisition of lands and completion of foundations by the contractor M/s LSML.
14	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,TELANGANA	12/2009	212.34 1,228.39	1,228.39	879.85	03/2013 09/2012	09/2015	30	478.5	i)Delay in supply of LW equipment ii)Delay in drive of gate roadways and installation of belt conveyors.
15	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67	2,675.67	1,648.31	03/2014	03/2016	24	0	i) Delay in procurement of major HEMM & construction of CHP & In-pit Conveyor transport system. ii) Rehabilitation & Resettlement problem
16	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH	12/2009	1,943.66	1,943.66	1,607.84	03/2014	03/2016	24	0	i) Delay in procurement of major HEMM & construction of CHP including Silo. ii) Rehabilitation & Resettlement problem
17	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,UTTAR PRADESH	06/2011	789.88	741.62	464.94	03/2013	03/2016	36	-6.11	i) Delay in land acquisition ii) Delay in Environment clearance iii) Coal evacuation problem
18	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,MADHYA PRADESH	06/2011	746.04	535.10	348.33	03/2015	03/2016	12	-28.27	

(March 2015)

						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
19	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	469.78 -	706.40	53.38	07/2012 -	03/2016	44	50.37	i) Law & Order ii) Environmental Clearance iii) Coal evacuation problem
20	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 -	259.40	12.52	03/2012 -	03/2016	48	0	i) Environment clearance ii) Coal evacuation
21	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35 -	462.35	273.72	03/2014 -	03/2016	24	0	Contractual Issues
22	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	55.48	03/2014 -	03/2016	24	0	i) Law & Order ii) Contractual Issues iii) Land acquisitions iv) Rehabilitation & Resettlement Problems
23	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24	0	i) Rehabilitation & Resettlement Problems ii) Environmental Clearance.
24	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	418.97	326.51	03/2012 -	03/2016	48	0	i) Delay in acquisition of private land ii) R & R problem iii) Law & order
25	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	181.19	36.60	03/2012 -	03/2016	48	0	i) Environmental Clearance ii) Land acquisition Problems iii) R & R problems
26	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	211.71	03/2014 -	03/2016	24	0	Environmental Clearance
27	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	35.68	03/2011 -	03/2016	60	0	i) Contractual Issues ii) Law & Order ii) Environmental Clearance
28	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	149.41	03/2012 -	03/2016	48	0	i) Rehabilitation & Resettlement Problems ii) Law & Order ii) coal evacuation Problems
29	RG OC -III EXTENSION (PHASE - II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	6.56	06/2015 -	03/2016	9	0	i) Land Acquisition ii) Rehabilitation & Resettlement Problems iii) Jallaram vague diversion
30	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	132.68	03/2010 -	03/2017	84	0	Coal Evacuation problem
31	ASHOK EXPN OCP CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	471.66 341.63	341.63	117.84	03/2011 -	03/2017	72	-27.57	i) Law & Order ii) Coal evacuation problems
32	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL	11/2006	287.18 -	287.17	142.59	03/2011 -	03/2017	72	0	i) Contractual Issues ii) environment clearance

(March 2015)

						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
33	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL, ODISHA	12/2007	457.77 -	457.77	162.21	03/2013 -	03/2017	48	0	i) Environmental Clearance ii) Coal evacuation Problems ii) Rehabilitations & Resettlement Problems
34	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]MCL, ODISHA	12/2007	172.08 -	172.08	148.02	03/2010 -	03/2017	84	0	Rehabilitations & Resettlement Issues
35	KAKATIYA LONGWALL - [N06000048]SCCL, TELANGANA	12/2008	453.63 -	453.63	104.49	12/2012 -	03/2017	51	0	i) Contractual Issues (TPO selection) ii) Adverse Geomining Conditions
36	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL, ODISHA	08/2008	207.28 -	207.28	172.80	03/2012 -	03/2017	60	0	i) Environmental Clearance ii) Delay in forest land Diversion
37	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.53 -	479.63	118.94	03/2013 -	03/2017	48	.02	Environmental Clearance
38	JAGANNATHPOR OC - [N06000075]SECL, CHHATISGARH	09/2008	152.43 -	152.43	21.55	03/2015 -	03/2017	24	0	i) Rehabilitations & Resettlement Problems ii) Environment clearance
39	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL, JHARKHAND	12/2007	179.87 -	179.87	75.71	03/2012 -	03/2017	60	0	i) Rehabilitations & Resettlement Problems ii) Law & order iii) Coal evacuation problems
40	KARMA OCP (1.0 MTY) - [N06000088]CCL, JHARKHAND	06/2009	162.46 -	162.46	69.64	03/2014 -	03/2017	36	0	i) Rehabilitations & Resettlement Problems ii) Law & Order iii) Authentication of land
41	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL, TELANGANA	07/2012	417.33 -	417.33	11.41	07/2016 -	03/2017	8	0	i) Land Acquisition ii) Rehabilitation & Resettlement Problems
42	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29 -	242.29	0.03	03/2015 -	03/2018	36	0	i) Land Acquisition ii) Rehabilitation & Resettlement Problems iii) Delay in diversion of forest land. iv) Environment clearance
43	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL, TELANGANA	07/2011	447.06 -	447.06	29.03	03/2015 -	03/2018	36	0	i) Land Acquisition ii) Rehabilitation & Resettlement Problems iii) Delay in diversion of forest land. iv) Environment clearance
44	NEYVELI NEW THERMAL POWER PROJECT (2X500 MW) - [N06000095]NLC, TAMIL NADU	06/2011	5,907.11 -	5,907.11	784.75	12/2015 04/2018	04/2018	28	0	Delay in opening and evaluation of bids
45	TALABIRA OCP - [N06000043]MCL, ODISHA	03/2008	447.72 -	447.72	52.36	03/2016 -	03/2020	48	0	Delay in Environment and forestry Clearance.
46	GOPAL PRASAD OCP (15 MTY) - [N06000042]MCL, ODISHA	02/2008	395.87 -	395.87	76.74	03/2015 -	03/2021	72	0	i) Rehabilitation & resettlement problems. ii) Environmental clearance
	Total		28,301.52 -	32,309.68	17,948.23					

(March 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	STEEL									
47	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]NMDC,CHHATISGARH	01/2007	607.17 -	607.17	386.96	12/2011 01/2015	03/2015	39	0	
48	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL,ANDHRA PRADESH	10/2005	8,692.00 12,291.00	12,291.00	11,284.83	10/2009 10/2012	05/2015	67	41.41	
49	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,JHARKHAND	05/2010	6,325.00 -	6,325.00	5,097.28	12/2011 -	05/2015	41	0	
50	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,WEST BENGAL	08/2010	2,875.00 -	2,875.00	2,567.13	12/2012 -	05/2015	29	0	
51	CAPTIVE POWER PLANT - 2 - [N12000087]RINL,ANDHRA PRADESH	02/2011	677.00 -	677.00	509.41	09/2013 -	05/2015	20	0	
52	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]RINL,MULTI STATE	07/2007	480.00 -	450.00	375.17	09/2009 05/2012	06/2015	69	-6.25	
53	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,KARNATAKA	04/2011	572.00 -	572.00	451.58	04/2013 09/2014	06/2015	26	0	
54	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL,ODISHA	11/2011	254.55 -	254.55	123.28	11/2013 -	06/2015	19	0	
55	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHHATISGARH - [N12000078]SAIL,CHHATISGARH	07/2012	332.65 -	332.65	172.77	08/2014 -	06/2015	10	0	
56	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL,ODISHA	10/2012	160.48 -	160.48	118.88	09/2014 -	06/2015	9	0	
57	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,KARNATAKA	02/2011	898.55 -	898.55	379.57	05/2013 01/2015	08/2015	27	0	
58	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA	12/2011	187.33 -	187.33	149.44	10/2013 -	08/2015	22	0	
59	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079]SAIL,ODISHA	06/2012	237.09 -	237.09	155.48	12/2014 -	08/2015	8	0	
60	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	14,300.13	03/2013 -	09/2015	30	0	

(March 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
61	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL,ANDHRA PRADESH	07/2011	877.73 -	877.73	164.04	07/2015 -	03/2016	8	0	
62	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH	01/2010	15,525.00 -	15,525.00	6,655.07	05/2015 12/2016	12/2016	19	0	
63	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL,ANDHRA PRADESH	05/2012	404.16 -	404.16	144.33	07/2015 -	03/2017	20	0	
	Total		56,370.71 -	59,939.71	43,035.35					
	<u>PETROCHEMICALS</u>									
64	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,ASSAM	04/2006	5,460.61 8,920.00	9,834.00	8,459.13	04/2012 12/2013	06/2015	38	80.09	
	Total		5,460.61 -	9,834.00	8,459.13					
	<u>PETROLEUM</u>									
65	PARADIP REFINERY PROJECT - [N16000058]IOCL,ODISHA	02/2009	29,777.00 34,555.00	34,555.00	28,733.70	11/2012 11/2013	03/2015	28	16.05	Initial change in Front End Engg Design due to deferment of Petrochemicals lead to delayed detailed engg and subsequent procurement, There was further delay of 14-25 months in getting Enviroment and Forest clearance of South Jetty and Pipeline.Law & Order at site, . Delay in construction of Power Plant by BHEL. Delay in delivery of Equipment/Bulk items by vendors due to overloading, liquidity crunch etc.Delay in remobilization of manpower after cyclone Phailin struck Paradip in Oct' 13.
66	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]ONGC,TRIPURA	07/2008	288.04 253.66	253.66	218.56	08/2012 03/2015	03/2015	31	-11.94	Construction of activities hampered due to ROU related issues. Marshy and highly undulating terrain resulting in poor progress in pipeline laying work.

(March 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
67	102 MW WIND POWER PROJECT - [N16000119]ONGC,RAJASTHAN	07/2010	1,106.00 678.02	678.02	405.00	06/2012 03/2015	03/2015	33	-38.7	Commissioning is pending as NOC is awaited from the MOD (air force). ROW problem at site due to intervention of local villagers. Work commenced under police protection.Scope revision and delay in award of work
68	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 761.68	761.68	728.35	05/2013 06/2014	03/2015	22	-11.62	Increase in scope of work.Delay in procurement of steel and fabrication of legs by the contractor.
69	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL,MAHARASHTRA	03/2012	1,419.00 -	1,419.00	1,108.86	12/2014 -	03/2015	3	0	Delay in environment clearance-EC since received in June'13. Delay in delivery of piping bulk and equipment by vendors.
70	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE	01/2012	352.49 -	352.49	104.58	03/2014 04/2015	04/2015	13	0	Design platform integrity issue was raised by the contractor which required review of integrity analysis and this took time in resolution. Clubbing of project facilities alongwith C-26 Cluster development project. slow progress by the contractor.
71	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,MAHARASHTRA	06/2007	3,248.78 5,633.44	6,000.00	5,925.40	08/2010 03/2012	05/2015	57	84.68	Contract terminated as contractor failed to submit PBG insurance. Splitting of facility into three packages, scope optimization in view of the price rise in oil field services/equipments and preparation of fresh bid packages. Completion of well platforms and process platform got delayed.
72	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC,MULTI STATE	11/2010	331.20 -	269.10	190.04	08/2013 05/2015	05/2015	21	-18.75	Delay in award of work. Slow progress by the contractors.Delay in supply of vessel due to custom bond issue.
73	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17 600.17	600.17	249.17	12/2014 05/2015	05/2015	5	0	contractor's inability to execute work in time. -Contractor is yet to establish LC for line pipe manufacturers. Several long lead items not yet ordered. Purchase orders issued earlier are expired. -In adequate resource mobilization .

(March 2015)

						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
74	PIPELINE REPLACEMENT PROJECT-3 - [N16000137]ONGC,MULTI STATE	04/2012	2,547.26 1,417.00	1,417.00	1,410.50	05/2014 05/2015	05/2015	12	-44.37	Technical issues encountered w.r.t. laying of balance 2 segment. Delay by contractor
75	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,MULTI STATE	04/2003	429.82 3,955.21	3,955.21	3,439.48	04/2006 04/2016	06/2015	110	820.2	Termination of Contract. Non-cooperation by equipments suppliers, sub-contractors and consultant.Delay in availability of subsea manifold and prolonged repairing work.Complications in well G-1-9 and well control activities.Delay in proceedings in Mumbai High Court and prolonged legal battle.Delay in finalisation of out of court settlement.. ONGC took over the project in 2010 after settlement with M/S CEL.
76	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00 -	2,915.00	1,339.14	12/2012 -	06/2015	30	0	Stiff resistance from farmers/ land owners and subsequent court proceedings stalled the pipeline laying in agricultural land.
77	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	429.00	278.78	06/2011 03/2012	07/2015	49	-7.41	Delay in award of pipeline laying works due to clarification sought by Petroleum and Natural Gas Regulatory Board and delay in 3 (i) Gazette notification.
78	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL,TAMIL NADU	12/2012	279.00 -	279.00	142.28	12/2014 06/2015	07/2015	7	0	Precommissioning activities are in progress. Hook up shutdown for Mounded bullet pipe lines are to be done during existing Refinery-III S/d which is planned in July 2015.
79	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	317.64 -	240.95	111.38	09/2012 04/2015	10/2015	37	-24.14	Slow progress in civil work and fabrication work due to less resource mobilization.Unresolved commercial issues between M/s UEM and NSF Vendor.Delay in finalization of Process package leading to delay in engg and procurement services. Delay in delivery of Nut Shell filters and internal of IGF units.

(March 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
80	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,ANDHRA PRADESH	01/2006	672.00 1,178.35	1,178.35	1,099.88	10/2011 -	10/2015	48	75.35	Completion delayed primarily because the rectification of rock wedge failure in cavern A1 took more time.Zones of poor geology encountered during excavation of balance bench.Slow construction progress of AG facility Works as it was dependent on completion of UG works.
81	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	944.84	10/2011 -	10/2015	48	67.62	Delay in finalization of crude filling and evacuation philosophy for Mangalore project. Delayed land acquisition for Mangalore.Delay in award.Slow construction progress of AG works
82	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,398.50	01/2012 -	10/2015	45	70.49	Delay in getting Order for Mangalore-Padur pipeline.Delay in preparation/approval of DFR.Delay in land acquisition. Delay in site surveys. Delay in finalization of Basic Engg and Detailed Engg.Delay in finalization of crude filling and evacuation philosophy
83	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]ONGC,MULTI STATE	10/2013	429.06 429.00	429.06	-	10/2014 10/2015	10/2015	12	0	
84	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	215.66	-	06/2012 11/2015	11/2015	41	-20.13	Delay in placement of order for 2 nos drilling rigs. One of the bidder went to court in anticipation of disqualification of their bid
85	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	736.65	472.24	09/2011 12/2015	12/2015	51	0	Delay in preparation of drawing and additional model testing of Hull form in Austria . Shortage of skilled manpower at contractor's end.Inadequate ancillary/sub-contractors at the locationLack of planning to match resources to work targets.Change in delivery location.Delay in procurement of steel by PSL.
86	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA	12/2009	1,584.00 -	1,584.00	1,193.37	08/2015 -	12/2015	4	0	

(March 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
87	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE	06/2010	2,523.00 2,523.00	2,523.00	1,019.79	01/2014 12/2015	12/2015	23	0	Slow progress by contractor. Slow progress by the contractor in laying of pipelines.Delay in conversion work of Sagar Samrat to MOPU.Delay in drilling of some wells due to non-availability of light rig.
88	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,MULTI STATE	08/2011	586.00 -	586.00	295.67	08/2015 -	12/2015	4	0	
89	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96 -	191.96	77.79	05/2015 -	12/2015	7	0	Project schedule is adversely affected due to delay in acquisition of additional land admeasuring 3.99 acre and limited availability of construction sand in Jharkhand due to existing regulations of State Government
90	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 1,200.00	1,200.00	180.26	03/2015 11/2015	02/2016	11	37.72	Heavy rain in Assam.Refloating of tender will have impact on timeline
91	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 -	2,378.89	1,768.09	03/2013 03/2015	03/2016	36	-3.5	Substantial time taken for mobilization by survey and other agency.ROU acquisition and issue related to payment. Delay in forest clearance.Inadequate manpower at working sites affected the construction progress.Local problem and court cases by tea gardener. Slow progress in engineering and procurement.
92	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	1,087.70	09/2012 -	03/2016	42	0	Project is delayed due to receipt of Forest clearance. Tree cutting permissions in Odisha awaited. Law and order problems.Poor performance by contractors.Fund constraint of Contractor.
93	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 2,592.17	2,592.17	534.59	05/2014 03/2016	03/2016	22	0	Delyed due to retendering. Package-1 delayed due to representation by M/s Essar in IEM. Slow progress by contractor
94	IMPROVED OIL RECOVERY OF B-173A FIELD - [N16000185]ONGC,MAHARASHTRA	01/2012	352.49 -	352.49	104.58	03/2014 -	03/2016	24	0	

(March 2015)

						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
95	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	854.43	03/2015 05/2016	05/2016	14	29.42	3. Contractor has made additional claim of change order of approximately Rs 550 Crore. -Arbitration with ONGC. -Contractor has not taken action on procurement, fabrication, identification of marine spread and has not finalized any subcontracting arrangements.
96	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	723.64	-	03/2013 06/2016	06/2016	39	0	Revision in scope of work.High quoted price resulting in closure of the original tender.
97	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 462.79	462.79	215.01	10/2014 10/2016	10/2016	24	49.38	Project commenced after getting PNGRP clearance on 01.11.2012
98	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,KARNATAKA	02/2012	666.00 838.00	838.00	443.65	11/2015 11/2016	11/2016	12	25.83	
99	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]ONGC,MAHARASHTRA	12/2012	3,513.07 4,619.94	4,619.94	0.47	02/2016 04/2017	04/2017	14	31.51	Revised scope of work
100	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	12/2012	607.06 607.06	607.06	57.79	01/2016 04/2017	04/2017	15	0	
101	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC,MULTI STATE	04/2013	284.82 -	284.82	-	04/2015 04/2015	05/2017	25	0	Retendering of work due to revised scope of work. constraints, regarding to lead times and Caisson installation.
102	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 -	188.89	2.00	01/2014 11/2017	11/2017	46	-6.92	Due to poor progress, contract terminated and re-tendering is in progress.

(March 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
103	AHMEDABAD REDEVELOPMENT PROJECT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10 -	1,916.10	1,161.74	12/2014 -	12/2017	36	0	Preparation of TBP and cost estimation takes too much time. Large no. of installations and non-availability of technical input such as as-built drawings, contour surveys and layout of control rooms etc.Preparation of pre-bid replies in view of the quantum and complexities.Several rounds of discussions/ clarifications with the bidders.Delay in land acquisitionProject has been dropped, Approved by ONGC Board in Feb-15.
104	MEHESANA REDEVELOPMENT PROJECT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	3,823.00	1,076.57	04/2015 12/2017	12/2017	32	0	Project has been dropped now.
105	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS - [N16000181]ONGC,MULTI STATE	03/2013	2,913.10 -	2,913.10	9.72	05/2016 04/2018	04/2018	23	0	re-invitation of tenders
106	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63 -	2,189.63	1,035.48	12/2014 -	12/2018	48	0	- Preparation of TBP and cost estimation - Large no. of installations and non-availability of technical input such as as-built drawings, contour surveys and lay out of control rooms etc. - Preparation of pre-bid replies in view of the quantum and complexities. -Several round of discussions/ clarification with the bidders. -Land Acquisition.
107	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18 -	7,596.18	17.06	01/2013 -	02/2019	73	0	No firm commitment from anchor laod customers.Non-availability originally envisaged RIL's KG D-6 Gas and ONGC's Mahanadi Gas at Haldia due to non-execution of Kakinada-Haldia pipeline
	Total		88,533.32 -	101,635.31	59,436.44					
	POWER									

(March 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
108	BARH STPP STAGE -II - [N18000047]NTPC,BIHAR	02/2008	7,341.04 -	7,341.04	8,594.00	10/2013 -	03/2015	17	0	Delay in supplies by BHEL. Boiler Metallurgical Issues & delay in Technology absorption by BHEL.
109	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATISGARH	05/2011	1,961.87 -	1,961.87	1,653.45	05/2014 -	03/2015	10	0	Delayed due to delay in land acquisition & Poor performance by contractor.
110	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL,MADHYA PRADESH	03/2012	213.78 -	213.78	190.44	03/2014 -	03/2015	12	0	Commissioning matching with TBCB lines (Pvt. lines).
111	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]PGCIL,MULTI STATE	09/2011	1,366.34 1,606.38	1,606.38	1,268.66	12/2013 04/2015	04/2015	16	17.57	Delayed due to delay in land acquisition for Vadodhara sub station.
112	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL,MULTI STATE	02/2012	1,927.16 -	1,927.16	1,462.27	10/2014 -	04/2015	6	0	Delayed due to delay in land acquisition of Pune GIS and severe ROW problem.
113	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,BIHAR	12/2011	901.77 1,025.28	1,025.28	867.80	08/2014 04/2015	04/2015	8	13.7	IROW problem.
114	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH	11/2011	2,127.51 -	2,127.51	2,129.33	07/2014 -	05/2015	10	0	Delayed due to severe ROW problem & forest clearance awaited.
115	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 2,228.71	2,228.71	863.63	08/2014 -	05/2015	9	27.6	Forest clearance awaited & non-readiness of Kudus s/stn. (MSETCL).
116	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	171.92	04/2015 -	05/2015	1	0	Delay in land acquisition for Varansai S/stn.
117	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]PGCIL,MULTI STATE	09/2012	803.34 -	803.34	544.89	03/2015 -	05/2015	2	0	ROW being encountered.
118	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]NEEPCO,TRIPURA	07/2012	296.87 363.73	363.73	309.52	12/2014 -	05/2015	5	22.52	

(March 2015)

						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
119	KOLDAM HEP (NTPC) - [180100211]NTPC,HIMACHAL PRADESH	10/2002	4,527.15 7,220.00	7,220.00	6,544.00	04/2009 -	06/2015	74	59.48	Geological surprises leading to huge change in scope. Contractual issues with M/s ITD leading to slow down of work & intermittent stoppage of work.
120	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 2,348.37	2,348.37	1,764.24	03/2013 06/2015	06/2015	27	13.18	Forest clearance & severe ROW problem.
121	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]PGCIL,MULTI STATE	03/2011	2,569.25 3,105.51	3,105.51	2,729.47	03/2014 06/2015	06/2015	15	20.87	Forest clearance/ wild life sanctuary clearane & severe ROW problem.
122	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	105.10	01/2013 -	06/2015	29	0	Delayed in land acquisition for Kishanganj Sub station.
123	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,407.46	11/2013 -	06/2015	19	0	Delayed due to delay in land acquisition & severe ROW problem faced demanding high compensation.
124	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,732.36	09/2014 -	06/2015	9	0	Severe ROW problem faced in Karnataka & contractual issue.
125	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	1,801.76	08/2014 -	06/2015	10	0	Delayed due to delay in land acquisition (acquired in Jun-14) and delay in forest clearance.
126	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 346.79	346.79	262.57	08/2014 06/2015	06/2015	10	16.63	Severe ROW problem in Bengalure area.
127	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	2,195.41	10/2014 -	06/2015	8	0	Delayed due to delay in land acquisition for Kanpur Sub station (land acquired in Jun-13).
128	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,MULTI STATE	06/2012	1,263.26 -	1,263.26	1,006.48	11/2014 -	06/2015	7	0	Severe ROW problem faced in Vijaywada - Nellore line.
129	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND - III GEN. PROJ. - [N18000076]PGCIL,MULTI STATE	03/2010	4,672.99 -	4,672.99	3,607.97	11/2012 -	07/2015	32	0	Severe ROW problem & Wildlife sanctuary /forest clearance awaited.Delayed land acquisition of Vindhychal PS.
130	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 -	994.85	898.22	07/2013 02/2011	08/2015	25	136.3	Gas turbine commissioning delayed due to non-supply of gas by ONGC

(March 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
131	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19 -	2,743.19	2,659.80	12/2013 -	09/2015	21	0	Delayed in forest clearance.
132	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	487.49	336.42	06/2014 -	09/2015	15	0	Severe ROW problem faced in Karnataka.
133	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	468.60	02/2014 -	09/2015	19	0	Severe ROW problem faced.
134	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,KARNATAKA	03/2005	1,007.16 -	1,007.16	970.31	12/2007 12/2009	12/2015	96	0	Severe ROW problem
135	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,MULTI STATE	09/2012	1,508.74 -	1,508.74	627.18	03/2015 -	12/2015	9	0	Due to delay in land acquisition for Kudgi S/stn.
136	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 721.81	721.81	515.79	09/2010 06/2013	12/2015	63	51.1	Severe ROW problem faced in Maharashtra & non readiness of Kudus sub station (MSETCL).
137	TRANSM SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 -	4,404.57	1,221.75	01/2015 -	12/2015	11	0	Delay in land acquisition for Alipurduar HVDC Station & Wild life sanctuary clearance.
138	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	719.74	11/2012 -	12/2015	37	0	Severe ROW problem in western UP.
139	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 -	752.64	473.82	07/2013 -	12/2015	29	0	Forest clearance awaited.
140	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	419.81	11/2013 -	12/2015	25	0	Forest clearance awaited. Delayed due to delay in land acquisition for sub station (Acquired in Apr-13).
141	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATTISGARH	01/2012	1,422.85 -	1,422.85	932.12	01/2015 -	12/2015	11	0	Forest clearance awaited. Critical
142	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATTISGARH	03/2012	9,569.76 -	9,569.76	3,874.59	06/2015 -	12/2015	6	0	Delayed due to delay in land acquisition (land acquired in Apr-13) & forest clearance awaited.

(March 2015)

						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
143	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	478.22	11/2014 -	12/2015	13	0	Delayed due to Terrain & climate constraints. Work severely affected due to flood in J&K.
144	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	664.43	06/2015 -	12/2015	6	0	Forest clearance awaited.
145	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	2,159.07	1,889.15	09/2008 03/2012	03/2016	90	21.34	Severe ROW problem
146	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99 1,487.49	1,487.49	994.41	08/2013 -	03/2016	31	159.15	
147	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	458.76	11/2011 -	03/2016	52	0	Severe ROW problem in western UP due to farmer agitation demanding high compensation.
148	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	313.27	02/2012 -	03/2016	49	0	Severe ROW problem in western UP due to farmer agitation demanding high compensation.
149	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	4,041.48	10/2012 -	03/2016	41	0	Forest clearance awaited & unsatisfactory performance by contractor.
150	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	10,130.80	08/2013 -	03/2016	31	0	Severe ROW problem due to agitation against Big Dam Project affecting works of line in Assam.Generation project delayed.
151	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	2,036.00	12/2012 -	03/2016	39	0	ROW problem/ disturbance & Insurgency, geographical constraints. Poor performance by contractor.
152	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,045.29	08/2012 -	03/2016	43	0	Severe ROW problem.
153	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,170.02	04/2013 -	03/2016	35	0	Severe ROW problem in western UP due to farmer agitation & delay in land acquisition for Bareilly sub station.
154	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	965.23	11/2012 -	03/2016	40	0	Delayed due to delay in land acquisition of sub stations & ROW problems.
155	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 -	155.57	-	03/2016 -	05/2016	2	0	

(March 2015)

						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
156	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]NHPC, WEST BENGAL	09/2005	1,061.38 -	1,929.15	1,715.90	09/2009 -	06/2016	81	81.76	1 Initial delay in handing over of forest land. 2 Bandh/ closure by locals, GJMM and its effect. 3 Contractual issues 4 Delay in award of E&M contract due to clarification regarding participation of Chinese firm.
157	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL, MULTI STATE	03/2012	198.63 -	198.63	16.00	09/2014 -	06/2016	21	0	Severe ROW problem.
158	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO, MIZORAM	07/1998	368.72 1,381.71	1,381.71	800.74	07/2006 12/2015	10/2016	123	274.73	
159	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC, JAMMU AND KASHMIR	01/2009	3,642.04 -	5,497.72	3,915.36	01/2016 -	11/2016	10	50.95	1. Law & order problem in the project area and Kashmir Valley. 2. Delay in settlement of R&R plan of the project which is pending with J&K State Govt. for approval and strike by PFA's 3. Due to delay decision of International Court of Arbitration
160	MOUDA STPP STAGE 2 - [N18000132]NTPC, MAHARASHTRA	03/2012	7,921.47 -	7,921.47	3,839.00	09/2016 -	02/2017	5	0	Delay in supplies & slow progress in erection activities of Steam Generator (M/s BHEL).
161	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO, ARUNACHAL PRADESH	12/2004	2,496.90 4,676.34	4,676.34	3,824.04	12/2009 03/2017	03/2017	87	87.29	
162	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC, ASSAM	01/2008	4,375.35 6,749.18	6,749.18	5,138.00	09/2011 -	03/2017	66	54.25	Inadequate deployment of manpower & resources by M/s BHEL and its sub-agencies have affected the erection/commissioning progress of U#1, Poor performance of BOP/Civil contractors due to geo-political situation in the region, Frequent Bandh calls by local outfits (Total Bandh-262 days) leading to stoppage of work at site for more than 500 days, Eruption of ethnic violence in Jul-12, May-14 & Dec-14 (41 days) leading to stoppage of work for 171 days

(March 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
163	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	01/2012	15,166.19 -	15,166.19	7,894.00	01/2017 -	03/2017	2	0	NGT issue – work stopped from 17.03.14 to 01.04.14 . Work stoppage due to agitation against the project (5.07.14 to 22.07.14)
164	FGUTPP, UNCHAHAH STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH	07/2013	3,363.12 -	3,363.12	510.00	12/2016 -	05/2017	5	0	Delay in award of BOP Packages by EPC agency M/s NBPPL.
165	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	4,571.00	11/2016 -	08/2017	9	0	Delay of 12 months in Engg. & supplies by BGR which has led to a consequent delay of 12 months in erection.
166	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 15,095.67	15,095.67	10,750.00	12/2009 10/2014	03/2018	99	73.65	Non performance of Russian agency M/s TPE & M/s PM. TPE stopped work from Oct-2013 and the contract of M/s TPE was terminated on 14.01.15.
167	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	1,189.01	07/2010 02/2016	05/2018	94	79.77	1.Non availability of Asena Quarry 2.Regular hindrances in Chopra dumping area 3.Fund crises with HCC civil contractor.
168	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	2,420.00	03/2013 -	05/2018	62	29.14	Flash Flood in Jun-12 in Uttarakhand leading to damage of coffer dam & approach road. Tunnel Boring Machine stuck up thrice & L&T Alpine JV did not perform leading to termination of contract. Head Race Tunnel (HRT) Package is under retender. U#1 Commissioning 3 years from award of HRT package, subsequent units a phase gap of one month.
169	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	3,745.08	592.40	07/2014 11/2018	11/2018	52	50.31	Frequent stoppage of works by local villagers and court cases

(March 2015)

						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
170	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	7,531.72	4,959.80	09/2009 -	12/2018	111	92.16	Initial delay in start of Dam works due to delay in Revised Forest clearance 2.Burial of TBM during Nov, 06. Heavy ingress of water with silt from TBM face. Treatment of shear zone, 3.Back hill slope failure of Power House three times, 4.Ban on use of aggregates by Hon'ble High Court, Shimla
	Total		164,942.11 -	193,265.62	131,653.19					
	<u>RAILWAYS</u>									
171	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	608.02	602.10	03/1994 -	03/2015	252	282.96	Authorisation from CRS for opening of new line for public carriage of passenger is awaited.
172	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	883.00	755.50	02/2009 -	03/2015	73	466.97	Fund is required.
173	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 393.46	1,026.00	181.48	03/2007 03/2007	03/2015	96	160.76	Land acquisition issue affected progress of projects.
174	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	432.72	436.85	12/2009 03/2011	06/2015	66	300.67	Not Reported
175	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII-MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	874.57	703.56	03/2013 -	09/2015	30	81.45	
176	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 -	207.52	223.44	12/2012 -	09/2015	33	0	Not Reported
177	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 245.39	245.39	249.33	12/2008 -	10/2015	82	104.49	Not Reported
178	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	335.00	230.67	06/2004 -	12/2015	138	72.62	Law & Order issue affected the work progress. Material Modification for Electrification estimate are awaited from Jharkhand Govt.
179	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 -	2,921.00	2,339.60	10/2007 12/2012	12/2015	98	367.76	Not Reported

(March 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
180	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	800.00	798.47	03/2010 -	12/2015	69	16.41	Not Reported
181	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 495.44	1,781.98	420.45	03/2004 12/2010	03/2016	144	259.68	Fund constraint affecting the progress of projects.
182	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	272.39	141.55	03/2012 12/2013	03/2016	48	59.2	Electrification work on the balance portion is in progress
183	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,069.60	34.87	03/2014 -	03/2016	24	-9.96	Fund constraints
184	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM	04/1998	227.90 200.00	331.40	182.22	12/2012 -	03/2016	39	45.41	Not Reported
185	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 -	5,500.00	4,734.45	03/2009 -	03/2016	84	228.1	Land acquisition issue.
186	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	583.00	144.66	12/2015 -	03/2016	3	88.4	Work delayed due to foundation problem.
187	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 575.00	1,242.25	1,005.81	03/2007 -	03/2016	108	38.8	Section will be completed after Lumding-Silchar, Badarpur- Kumarghat GC Project.
188	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	143.73	03/2016 -	06/2016	3	0	Work hampered due to encroachment on Railway land along the proposed metro alignment.
189	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	230.00	68.67	03/2015 -	12/2016	21	53.44	Not Reported
190	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 -	1,564.54	420.71	03/2010 03/2017	03/2017	84	381.4	Not Reported
191	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	714.10	59.18	04/2016 -	03/2017	11	0	Not Reported
192	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 1,000.00	4,996.19	3,410.06	04/2008 03/2014	06/2017	110	233.08	Not Reported

(March 2015)

						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
193	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	1,727.27	743.74	12/2010 -	03/2018	87	250.37	Work affected due to fund constraint.
194	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	733.00 733.00	2,531.34	1,732.43	12/2008 -	03/2018	111	245.34	Work is affected due to land problems.
195	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 813.34	2,876.00	823.83	03/2014 -	03/2018	48	253.6	Supreme court approval is required for NBWL clearance.
196	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34 619.34	2,820.25	199.31	04/2014 03/2015	03/2018	47	355.36	Not Reported
197	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP,TELANGANA	04/2012	632.68 -	816.55	42.58	03/2016 -	03/2018	24	29.06	Not Reported
198	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	19,565.00	10,658.34	11/2002 -	12/2018	193	682.6	Not Reported
199	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 727.56	6,570.75	2,787.99	03/2011 03/2014	03/2019	96	803.12	Not Reported
200	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 6,213.84	6,821.29	2,217.14	03/2014 03/2019	03/2019	60	28.7	Fund constraint affecting the progress of projects.
201	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,157.54	1,544.40	590.26	03/1998 -	12/2019	261	299.79	Fund constraint & increase in scope of work.
202	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,WEST BENGAL	03/1998	111.90 1,039.29	2,371.85	486.25	03/2005 12/2008	12/2019	177	2019.62	Local disturbance and fund constraint affected the work progress.
203	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 1,013.74	1,428.00	466.36	06/2005 07/2011	12/2019	174	385.76	Land acquisition issue affected the work progress.
204	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 1,339.48	4,190.00	88.56	12/2015 -	03/2020	51	212.81	Delay in land acquisition affected the work progress.
205	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00 -	2,973.42	10.44	03/2015 03/2020	03/2020	60	249.81	Land acquisition is pending.
	Total		29,092.11 -	86,252.51	38,134.59					
	<u>ROAD TRANSPORT AND HIGHWAYS</u>									
206	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 157.47	154.57	268.50	09/2007 03/2014	03/2015	90	-1.84	

(March 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
207	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	201.66	191.80	09/2008 -	03/2015	78	30.1	Land acquisition Removal of archaeological structures. Poor performance of the contractor.
208	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	264.72	315.90	06/2008 -	03/2015	81	0	
209	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	245.00	491.20	03/2008 03/2015	03/2015	84	0	
210	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	198.16	345.80	04/2008 01/2015	03/2015	83	0	Land acquisition Utility shifting Slow progress by contractor Forest clearance
211	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	200.00	290.00	06/2008 -	03/2015	81	0	
212	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	792.06	1,983.00	12/2012 -	03/2015	27	0	
213	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	625.07	995.90	01/2013 -	03/2015	26	0	
214	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,425.00	06/2013 -	03/2015	21	0	
215	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	-	08/2014 -	03/2015	7	0	
216	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	632.70	02/2013 -	03/2015	25	0	
217	SIX LANNING OF HOSUR-KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	535.00	52.18	12/2013 -	03/2015	15	0	
218	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	381.50	06/2013 -	03/2015	21	0	
219	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	759.90	01/2014 -	03/2015	14	0	
220	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	408.10	04/2014 -	03/2015	11	0	
221	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	835.00	476.40	01/2014 -	03/2015	14	0	Delayed due to GIB sanctuary clearance from Supreme court. Land acquisition. Grave Yard clearance. Utility shifting
222	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	500.29	633.30	08/2013 -	03/2015	19	0	
223	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	909.00	982.90	05/2014 -	03/2015	10	0	

(March 2015)

						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
224	JAIPUR-REENGUS - [N24000198]NHAI, RAJASTHAN	08/2010	267.81 -	267.81	699.60	02/2013 -	03/2015	25	0	
225	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI, MAHARASHTRA	04/2012	484.19 -	484.19	285.50	10/2014 -	03/2015	5	0	
226	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI, BIHAR	07/2012	356.40 -	356.40	-	07/2014 -	03/2015	8	0	
227	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI, UTTAR PRADESH	10/2012	250.50 -	250.50	65.26	10/2014 -	03/2015	5	0	
228	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI, UTTAR PRADESH	01/2013	373.47 -	373.47	28.51	07/2014 -	03/2015	8	0	
229	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI, GUJARAT	03/2012	828.00 -	828.00	52.01	09/2014 -	03/2015	6	0	
230	REENGUS SIKAR - [N24000227]NHAI, RAJASTHAN	03/2012	333.51 -	333.51	152.50	09/2014 -	03/2015	6	0	
231	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, ASSAM	12/2003	175.96 -	175.96	290.20	04/2008 04/2015	04/2015	84	0	
232	NALBARI TO BIJINI (AS-6) - [N24000047]NHAI, ASSAM	12/2003	225.00 -	225.00	276.70	06/2008 04/2015	04/2015	82	0	Land acquisition Utility Shifting Slow progress by contractor
233	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, MULTI STATE	12/2003	604.00 -	604.00	495.40	12/2009 -	04/2015	64	0	
234	KOTA BYPASS, RJ-4, NH-76 (NHAI) - [240106297]NHAI, RAJASTHAN	12/2003	275.00 -	250.39	285.30	10/2008 -	05/2015	79	-8.95	
235	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI, TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,374.00	12/2013 -	05/2015	17	0	
236	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI, TAMIL NADU	05/2010	374.00 -	374.00	148.80	05/2013 -	05/2015	24	0	
237	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI, BIHAR	05/2011	511.54 -	511.54	1,179.00	11/2013 -	05/2015	18	0	
238	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, ASSAM	12/2003	199.81 -	385.13	159.20	04/2009 -	06/2015	74	92.75	
239	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, ASSAM	12/2003	167.64 -	167.64	180.30	11/2008 -	06/2015	79	0	

(March 2015)

						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
240	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	280.13	173.80	11/2008 -	06/2015	79	80.68	
241	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	200.00	207.60	04/2009 -	06/2015	74	0	
242	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	332.94	550.30	09/2008 -	06/2015	81	0	
243	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	211.80	05/2008 06/2015	06/2015	85	0	
244	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	331.23	242.10	07/2009 -	06/2015	71	68.99	
245	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	465.50	322.70	09/2007 -	06/2015	93	33.7	Land acquisition Forest clearance Permission of Railways for 4 ROBs.
246	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	667.10	05/2010 -	06/2015	61	0	
247	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	572.30	886.90	10/2011 -	06/2015	44	0	Improper planning of resources by contractor
248	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	650.00	1,178.00	11/2013 -	06/2015	19	0	
249	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	1,141.00	2,445.00	08/2013 -	06/2015	22	0	
250	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	942.90	07/2013 -	06/2015	23	0	
251	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	624.00	333.72	04/2014 -	07/2015	15	0	
252	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	195.00	280.30	06/2008 -	08/2015	86	0	
253	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	237.80	328.60	06/2008 -	09/2015	87	0	
254	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	795.00	1,133.00	05/2012 -	09/2015	40	0	
255	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	1,173.00	07/2013 -	09/2015	26	0	
256	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	398.00	462.00	02/2014 -	09/2015	19	0	Project abandoned by contractor

(March 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
257	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, BIHAR	05/2011	664.00 -	664.00	776.40	02/2014 -	10/2015	20	0	
258	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT	03/2010	1,509.10 -	1,509.10	2,686.00	09/2012 -	11/2015	38	0	
259	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	11/2015	48	106.5	
260	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, BIHAR	09/2011	574.00 -	574.00	991.70	03/2014 -	11/2015	20	0	
261	BEAWAR-PALI-PINDWARA - [N24000199]NHAI, RAJASTHAN	12/2011	2,388.00 -	2,388.00	2,301.00	06/2014 -	11/2015	17	0	
262	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI, KERALA	04/2011	682.00 -	682.00	752.70	10/2013 -	11/2015	25	0	
263	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI, ASSAM	12/2003	230.00 -	230.00	251.50	06/2005 -	12/2015	126	0	
264	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, ASSAM	12/2003	280.00 -	361.00	366.80	02/2009 -	12/2015	82	28.93	
265	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, ASSAM	12/2003	208.00 230.00	208.00	334.80	04/2008 04/2015	12/2015	92	0	Land acquisition Utility Shifting Poor planning by contractor
266	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061]NHAI, ASSAM	12/2003	212.00 -	212.00	127.10	09/2007 -	12/2015	99	0	
267	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI, MULTI STATE	12/2003	232.45 -	232.45	317.70	09/2010 -	12/2015	63	0	
268	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI, MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	12/2015	32	0	
269	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, TAMIL NADU	09/2010	852.00 -	852.00	901.60	03/2013 -	12/2015	33	0	
270	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	996.80	05/2013 -	12/2015	31	0	Improper planning and Cash flow problem with concessionaire Land acquisition
271	PUNE-SATARA(NH-4) - [N24000156]NHAI, MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,292.00	03/2013 -	12/2015	33	0	
272	INDORE-DEWAS(NH-3) - [N24000159]NHAI, MADHYA PRADESH	11/2010	325.00 -	325.00	611.80	05/2013 -	12/2015	31	0	

(March 2015)

						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
273	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	363.00	08/2013 -	12/2015	28	0	
274	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	805.39	842.20	03/2013 -	12/2015	33	0	
275	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	2,188.00	05/2014 -	12/2015	19	0	
276	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	835.60	07/2013 -	12/2015	29	0	
277	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	323.00	06/2014 -	12/2015	18	0	
278	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	209.00	38.77	01/2013 -	12/2015	35	0	Land acquisition Forest clearance Poor progress by the contractor
279	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	4,030.00	09/2013 -	12/2015	27	0	
280	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	593.50	03/2013 -	12/2015	33	0	
281	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	1,047.00	295.70	06/2014 -	12/2015	18	0	
282	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	1,396.18	1,934.00	09/2014 -	12/2015	15	0	
283	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	141.30	01/2014 -	12/2015	23	0	Land acquisition Tree cutting. Utility shifting. Poor performance by contractor.
284	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	478.00	328.70	10/2013 -	12/2015	26	0	
285	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	942.69	286.80	06/2014 -	12/2015	18	0	Inadequate mobilization of resources by contractor. Forest clearance. Land related issues
286	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	309.56	457.70	04/2010 01/2016	01/2016	69	42.25	
287	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00 -	1,232.00	87.61	08/2015 -	02/2016	6	0	
288	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	156.90	08/2012 -	03/2016	43	0	Funds constraint of contractor

(March 2015)

						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
289	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	-	10/2013 -	03/2016	29	0	
290	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	593.00	761.30	07/2013 -	04/2016	33	0	
291	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	1,928.22	647.40	04/2015 -	04/2016	12	0	
292	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	353.37	446.20	10/2011 -	06/2016	56	0	
293	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,170.00	07/2015 -	06/2016	11	0	
294	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	2,159.00	622.70	06/2015 -	06/2016	12	0	
295	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	929.60	09/2014 -	06/2016	21	0	
296	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,MULTI STATE	12/2012	1,479.00 -	1,479.00	368.60	06/2015 -	06/2016	12	0	
297	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	1,078.84	1,922.00	08/2013 -	08/2016	36	0	
298	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	588.40	02/2014 -	08/2016	30	0	
299	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	1,655.00	655.20	09/2013 -	11/2016	38	0	
300	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	193.45	66.11	11/2012 -	12/2016	49	0	Slow progress of work by contractor. Termination and re-award of contract
301	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	39.55	09/2013 -	12/2016	39	0	
302	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2016	35	0	
303	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	281.31	180.10	02/2010 -	02/2017	84	2.29	
304	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	726.40	07/2014 -	02/2017	31	0	
305	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	1,287.95	540.40	11/2015 -	03/2017	16	0	

(March 2015)

						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
306	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,138.00	03/2014 -	04/2017	37	0	
307	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	580.43	450.70	08/2013 -	05/2017	45	0	
308	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	998.79	1,610.00	08/2013 -	07/2017	47	0	
309	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	867.00	598.60	02/2015 -	12/2017	34	0	
	Total		77,042.07 -	78,983.46	71,759.42					
	<u>TELECOMMUNICATIONS</u>									
310	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL,ASSAM	06/2007	336.81 -	336.81	195.94	01/2009 -	03/2015	74	0	
311	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	384.00	54.97	10/2010 08/2015	09/2015	59	0	
	Total		720.81 -	720.81	250.91					
	<u>URBAN DEVELOPMENT</u>									
312	C/O MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB - [N28000070]CPWD,PUNJAB	08/2005	191.24 -	191.24	9.91	08/2007 -	03/2015	91	0	
313	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	205.00	97.61	03/2012 -	04/2015	37	0	1. Encroachment at both the sites. 2. Non availability of adequate funds during 2011-11(only 9.8 Crore), 2011-12(only 19.37 Crore), 2012-13(only 33.99 Crore) 2013-14(only 38.66 Crore) and 2014-15(only 12 Crore), Restriction of Expenditure and slow progress. 3. Heavy rains making expansive soil marshy and unapproachable for vehicular movement. 4. Raft foundation at 3 M because of poor bearing capacity. 5. Technical buildings works could not be started since MHA consultant did not provide complete details.
314	FARIDABAD EXTENSION - [N28000057]DMRCL,DELHI	09/2011	2,494.00 -	2,494.00	1,164.03	09/2014 -	05/2015	8	0	

(March 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
315	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD,WEST BENGAL	01/2009	225.81 -	225.81	17.60	06/2012 -	06/2015	36	0	Progress of balance work was hampered due to heavy rains and consequent water logging of site and change in decision by the Client department. Scheme of Electrical Services particularly HVAC work was changed after detailed elaboration and award of work was delayed due to General Election in May 2014.
316	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD,ODISHA	11/2012	238.43 -	238.43	-	02/2015 -	08/2015	6	0	Finalization of flooring work in 1st year lab building and approval of sample flat for Grade- A qtr from client awaited.
317	C/O NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 -	315.00	88.54	06/2015 -	08/2015	2	0	Initial Delay due to time taken in finalisation of Drawings by Architect/ Client
318	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	24.71	11/2014 -	10/2015	11	0	Pre-Construction: 1. Late approval of BOQ by IIT=3 Months. 2. Work awarded in 2nd call=2 Months. Post-Construction: 1. Late approvals: drawings from client (TCPO-21.10.13, Structural drws-24.12.13, LOP: 06.02.14, EIA approval; 21.2.14)= 4 Months. 2. Client not agreed contractual action for 6 bldg--1.5 Month. 3. 9 Blocks still not cleared by IIT= 1.5 Months. 4. Retaining walls details not issued yet by IIT=3 Months. 5. Abnormal winter rains-2014, 2015
319	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85 -	261.85	131.77	05/2013 -	11/2015	30	0	Initial delay of 1 year in availability of site, subsequent delay due to non-uniform flow of funds during 2012-13 & 2013-14, delay in finalization of interior scheme, non-availability of full site till date, non-performance of Interior Agency

(March 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
320	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL, MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	12/2015	11	0	
321	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD, DELHI	05/2012	405.01 -	405.01	-	12/2014 -	04/2016	16	0	Extra time involved in finalization of tender for addressing certain issues of client department.
322	2000 BOYS HOSTEL (1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD, JHARKHAND	09/2012	171.86 -	171.86	-	03/2016 -	05/2016	2	0	
323	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD, WEST BENGAL	02/2014	156.57 -	156.57	-	09/2015 -	07/2016	10	0	NR
324	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL, TAMIL NADU	02/2009	14,600.00 -	14,600.00	-	12/2015 -	08/2016	8	0	
325	DELHI MRTS PHASE-III - [N28000056]DMRCL, DELHI	09/2011	38,585.00 -	38,585.00	14,321.39	03/2016 -	12/2016	9	0	
326	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD, MADHYA PRADESH	12/2012	188.87 -	188.87	24.44	12/2014 -	12/2016	24	0	The master layout plan was approved first time by the Client department in Feb. 2012 but it was modified thrice during 2013-14 and finally approved on 13-02-2014
327	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD, TAMIL NADU	04/2014	332.72 -	332.72	0.11	09/2016 -	12/2016	3	0	NR
328	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD, DELHI	07/2012	884.30 -	884.30	103.45	08/2014 -	06/2017	34	0	The work was terminated on 24-07-2014 because of the non performance of the contractor for the first package. However, the tender for balance items of the package I along with package III has been awarded and work started at site.
	Total		82,662.49 -	82,662.49	15,983.56					
	Grand Total		575,226.70	699,233.46	421,312.39					

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(March 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	22,462.00	12/2008 -	07/2015	70.54
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	09/2016	62.57
	Total		16,663.00 -	28,139.00			
	<u>CIVIL AVIATION</u>						
3	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]	05/2010	335.61 -	388.53	05/2012 -	03/2015	15.77
	Total		335.61 -	388.53			
	<u>COAL</u>						
4	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,477.21	06/2009 -	04/2015	71.23
5	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37
6	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	09/2015	478.50
7	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,602.74	03/2012 -	04/2015	34.63
8	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	479.63	03/2013 -	03/2017	0.02
9	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	03/2016 -	03/2016	31.87
	Total		8,247.56 -	12,692.96			
	<u>PETROCHEMICALS</u>						
10	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	9,834.00	04/2012 -	06/2015	80.09
	Total		5,460.61 -	9,834.00			
	<u>PETROLEUM</u>						
11	DEV OF G1 AND GS-15 (ONGCL) - [160100231]	04/2003	429.82 -	3,955.21	04/2006 -	06/2015	820.20
12	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]	06/2007	3,248.78 -	6,000.00	08/2010 03/2012	05/2015	84.68

(March 2015)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
13	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00 -	34,555.00	11/2012 -	03/2015	16.05
14	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]	03/2010	4,550.40 -	6,638.94	03/2013 -	02/2015	45.90
15	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	05/2016	29.42
16	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	03/2012	14,225.00 -	16,504.00	05/2016 -	05/2016	16.02
17	REWARI KANPUR PIPELINE PROJECT - [N16000145]	02/2012	1,210.64 -	1,446.34	11/2015 -	11/2015	19.47
18	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	02/2012	666.00 -	838.00	11/2015 -	11/2016	25.83
19	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79	10/2014 -	10/2016	49.38
20	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]	01/2006	672.00 -	1,178.35	10/2011 -	10/2015	75.35
21	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]	01/2006	732.00 -	1,227.00	10/2011 -	10/2015	67.62
22	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]	12/2012	3,513.07 -	4,619.94	02/2016 -	04/2017	31.51
23	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	450.55	03/2017 -	03/2017	27.79
24	MARKETING TERMINAL AT PARADEEP - [N16000168]	07/2009	199.75 -	239.73	07/2013 -	-	20.02
25	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	10/2015	70.49
26	KOTA JOBNER PIPELINE PROJECT - [N16000170]	04/2011	276.26 -	276.27	12/2015 -	03/2015	0.00
27	MARKETING TOP AT KORBA - [N16000186]	01/2011	141.86 -	232.00	09/2016 -	12/2015	63.54
28	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	06/2014	5,706.47 -	5,813.25	05/2017 -	05/2017	1.87
29	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	02/2016	37.72
	Total		69,935.40 -	89,996.02			
	<u>POWER</u>						
30	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	7,531.72	09/2009 -	12/2018	92.16
31	KOLDAM HEP (NTPC) - [180100211]	10/2002	4,527.15 -	7,220.00	04/2009 -	06/2015	59.48
32	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	15,300.00	09/2010 -	-	143.42
33	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	4,676.34	12/2009 06/2016	03/2017	87.29
34	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	15,095.67	12/2009 -	03/2018	73.65

(March 2015)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
35	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243	09/2005	1,061.38 -	1,929.15	09/2009 -	06/2016	81.76
36	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258	05/2005	1,779.29 -	2,159.07	09/2008 -	03/2016	21.34
37	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	07/2006	1,657.00 -	2,978.86	07/2010 -	05/2018	79.77
38	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014	11/2006	2,978.48 -	3,846.30	03/2013 -	05/2018	29.14
39	KISHANGANGA HEP (3X110 MW) - [N18000031	01/2009	3,642.04 -	5,497.72	01/2016 -	11/2016	50.95
40	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035	12/2007	477.69 -	721.81	09/2010 -	12/2015	51.10
41	BONGAIGAON THERMAL POWER PROJECT - [N18000041	01/2008	4,375.35 -	6,749.18	09/2011 -	03/2017	54.25
42	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042	08/2008	2,491.58 -	3,745.08	07/2014 -	11/2018	50.31
43	PARE HYDRO ELECTRIC PROJECT - [N18000045	12/2008	573.99 -	1,487.49	08/2013 -	03/2016	159.15
44	TRIPURA GAS BASED POWER PROJECT - [N18000071	07/2009	421.01 -	994.85	07/2013 -	08/2015	136.30
45	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087	09/2010	2,074.86 -	2,348.37	03/2013 -	06/2015	13.18
46	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096	03/2011	2,569.25 -	3,105.51	03/2014 -	06/2015	20.87
47	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH [N18000105	09/2011	1,366.34 -	1,606.38	12/2013 -	04/2015	17.57
48	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115	12/2011	297.33 -	346.79	08/2014 -	06/2015	16.63
49	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH [N18000116	12/2011	1,746.65 -	2,228.71	08/2014 -	05/2015	27.60
50	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119	07/1998	368.72 -	1,381.71	07/2006 02/2015	10/2016	274.73
51	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127	12/2011	901.77 -	1,025.28	08/2014 -	04/2015	13.70
52	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) [N18000156	07/2012	296.87 -	363.73	12/2014 -	05/2015	22.52
	Total		55,001.54 -	92339.72			
	<u>RAILWAYS</u>						
53	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007	04/1986	158.77 274.56	608.02	03/1994 -	03/2015	282.96
54	VIRAMGAM-BHILDI(WR),GC - [220100062	04/1990	155.66 -	548.01	- 03/2010	-	252.06
55	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	925.30	- -	02/2014	643.63

(March 2015)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
56	AMRAVATI-NARKHER NL(CR) - [220100118	06/1994	663.01 175.30	725.00	06/1999 -	07/2012	9.35
57	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60
58	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135	04/1983	36.80 274.41	1,336.57	- -	03/2019	3,531.98
59	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	968.60	12/2012 -	-	218.62
60	CALICUT-MANGALORE (DL) (SR) - [220100151	02/1996	240.00 -	579.37	- -	02/2012	141.40
61	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	1,781.98	03/2004 -	03/2016	259.68
62	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181	02/1997	514.68 -	2,820.00	- -	-	447.91
63	HASSAN-BANGALORE VIA SHRAVANA- BELGOLA(NL),SWR - [220100183	02/1997	295.00 -	1,289.92	- -	-	337.26
64	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,544.40	03/1998 -	12/2019	299.79
65	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
66	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	800.00	- -	-	414.30
67	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192	03/1996	155.74 164.36	883.00	02/2009 -	03/2015	466.97
68	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	- -	-	840.53
69	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197	03/1997	677.97 1,062.36	1,651.54	- -	03/2015	143.60
70	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	06/2017	233.08
71	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	645.00	- -	03/2015	195.55
72	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	03/2015	160.76
73	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	335.00	06/2004 -	12/2015	72.62
74	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
75	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	247.66 -	1,630.97	05/2008 -	-	558.55
76	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240	04/1997	501.69 335.77	1,043.56	03/2012 -	-	108.01
77	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	12/2009 -	06/2015	300.67
78	KATI HAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	492.98 -	1,727.27	12/2010 -	03/2018	250.37
79	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	550.00 -	1,566.00	- -	-	184.73

(March 2015)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
80	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	844.00	- 05/2009	03/2015	248.16
81	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR- NAUTANWA GC (NER) - [220100255	04/1997	863.23 -	1,072.51	- -	06/2015	24.24
82	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	625.30 408.76	847.75	06/2007 -	-	35.57
83	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	980.00	- -	-	880.00
84	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) - [220100263	03/1998	280.00 -	1,122.00	- -	-	300.71
85	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	330.00 -	1,047.00	- -	-	217.27
86	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	2,531.34	12/2008 -	03/2018	245.34
87	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM- NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
88	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	02/2011 -	-	191.48
89	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	04/1996	138.00 -	1,382.78	- -	-	902.01
90	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	2,371.85	03/2005 12/2008	12/2019	2,019.62
91	JIND-SONEPAT (NL),NR - [220100280	01/2004	238.56 -	740.00	03/2012 -	12/2012	210.19
92	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	470.21 -	1,995.25	- -	-	324.33
93	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06
94	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	288.00	02/2009 02/2009	08/2014	73.33
95	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	6,570.75	03/2011 -	03/2019	803.12
96	KOSI BRIDGE (NL), ECR - [220100304	04/2002	322.95 -	341.41	03/2012 -	-	5.72
97	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	03/2009 -	12/2014	156.57
98	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76
99	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314	04/2001	470.92 727.13	1,225.90	- -	03/2017	160.32
100	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315	01/2004	915.70 -	3,700.00	- -	03/2015	304.06
101	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316	04/2003	218.19 -	343.00	- -	-	57.20
102	ETAWAH-MAINPURI (NL),NCR - [220100318	04/1997	120.00 -	245.39	12/2008 -	10/2015	104.49

(March 2015)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
103	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	1,101.16	- -	03/2017	186.92
104	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	818.29	02/2015 -	02/2015	346.59
105	CUTTACK - BARANG (LD) - [220100326	04/1995	127.13 -	225.00	- -	10/2014	76.98
106	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	276.00	03/2009 03/2009	08/2014	106.88
107	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	810.78 -	810.80	- -	-	0.00
108	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329	04/2003	136.62 -	289.93	12/2007 03/2010	-	112.22
109	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	332.92 283.95	477.88	03/2012 -	-	43.54
110	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032	04/2006	378.56 -	791.59	- -	-	109.11
111	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045	03/1997	261.70 -	280.00	02/2006 -	-	6.99
112	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049	07/2006	743.00 -	1,117.11	03/2008 06/2008	-	50.35
113	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075	09/2006	324.90 -	385.54	03/2010 -	-	18.66
114	BHOPAL BINA 3D LINE DOUBLING - [N22000077	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41
115	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' -AGASTIYAMPALLI [N22000079	09/2007	404.19 -	1,383.45	- -	-	242.28
116	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080	09/2006	343.17 -	914.98	- -	03/2015	166.63
117	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082	12/2006	170.00 -	485.00	03/2011 -	-	185.29
118	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084	09/2006	125.00 -	490.00	- -	-	292.00
119	TIDIVANAM-NAGARI (NL) - [N22000085	09/2006	456.00 -	1,080.00	- -	-	136.84
120	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086	09/2006	200.00 -	496.24	- -	03/2017	148.12
121	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087	09/2006	300.00 -	827.73	- -	03/2019	175.91
122	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	04/2006	325.00 -	1,564.54	03/2010 -	03/2017	381.40
123	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	04/2008	5,300.00 -	6,821.29	03/2014 -	03/2019	28.70
124	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094	02/2008	171.10 -	272.39	03/2012 -	03/2016	59.20
125	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097	03/1984	293.97 -	1,428.00	06/2005 -	12/2019	385.76
126	AGARTALA SABROOM, NL, NEFR - [N22000099	04/2008	813.34 -	2,876.00	03/2014 -	03/2018	253.60

(March 2015)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
127	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,820.25	04/2014 -	03/2018	355.36
128	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	565.13	- -	03/2018	99.75
129	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,190.00	12/2015 -	03/2020	212.81
130	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]	04/2007	482.00 -	874.57	03/2013 -	09/2015	81.45
131	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	653.55	03/2014 -	-	0.06
132	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012 -	-	135.68
133	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	-	1.06
134	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	850.00 -	2,973.42	03/2015 -	03/2020	249.81
135	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) [N22000125]	04/2006	117.36 196.95	196.95	03/2011 -	-	67.82
136	KATAKHAL TO BHAIKABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41
137	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT [N22000127]	04/1996	1,676.31 -	5,500.00	03/2009 -	03/2016	228.10
138	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	494.92	- -	-	67.77
139	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	913.48	- -	-	184.87
140	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	685.17	- -	-	53.63
141	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	3,500.00	- -	-	68.05
142	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	02/2020	226.98
143	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	262.00	- -	-	10.58
144	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]	04/2013	456.00 -	855.16	- -	-	87.54
145	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	-	17.92
146	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	218.39	- -	-	2.34
147	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	02/2019	226.23
148	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00	- -	-	62.32

(March 2015)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
149	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00	- -	12/2019	82.25
150	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
151	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44
152	DANGOAPSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	03/2016	88.40
153	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	12/2017	41.36
154	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
155	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
156	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
157	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00 -	1,887.90	- -	03/2019	5.00
158	ATTIPPATTU-PUTTUR - [N22000184]	04/2008	446.87 -	528.00	- -	-	18.16
159	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,200.00	- -	-	129.22
160	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
161	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17
162	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]	04/1998	271.24 -	520.00	- -	-	91.71
163	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,280.83	- -	-	55.74
164	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
165	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	563.13	- -	03/2019	154.33
166	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,242.25	03/2007 -	03/2016	38.80
167	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00 -	886.65	- -	03/2018	251.85
168	DIMAPUR-TIZIT NL - [N22000196]	04/2013	4,274.00 -	4,487.70	- -	-	5.00
169	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77 -	441.45	- -	03/2018	110.44
170	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	288.81	- -	03/2018	1.86
171	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22	- -	-	109.04
172	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	-	173.71

(March 2015)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
173	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202	04/2007	247.00 -	951.24	- -	03/2015	285.12
174	CHENGANNUR-CHINGAVANAM - [N22000203	04/2006	191.72 -	222.95	- -	-	16.29
175	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205	04/2010	4,083.02 -	5,307.90	- -	03/2020	30.00
176	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206	04/2010	242.22 -	679.57	- -	03/2018	180.56
177	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207	04/2010	241.52 -	394.28	- -	03/2017	63.25
178	MURKONGSELEK-PASIGHAT NL - [N22000208	04/2011	165.82 -	435.58	- -	03/2018	162.68
179	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209	04/1999	523.17 -	1,653.55	- -	03/2018	216.06
180	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210	04/2011	312.12 -	453.10	- -	03/2018	45.17
181	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211	04/2012	246.07 -	364.06	- -	03/2019	47.95
182	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213	04/2012	632.68 -	816.55	03/2016 -	03/2018	29.06
183	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215	04/2011	601.43 -	800.00	- -	-	33.02
184	WARDHA-NANDED MAHARASHTRA - [N22000231	04/2008	499.30 -	2,501.05	- -	-	400.91
185	KALYAN-KASARA 3RD LINE - [N22000233	04/2011	277.70 -	279.70	- -	-	0.72
186	PEN ROHA DOUBLING - [N22000254	04/2007	98.74 -	203.00	- -	03/2015	105.59
187	PANVEL PEN DOUBLING - [N22000255	04/2006	96.16 -	260.16	- -	01/2015	170.55
188	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256	04/2011	913.00 -	1,801.01	- -	-	97.26
189	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257	04/2007	179.65 -	1,350.91	- -	-	651.97
190	BAGALKOT-KUDACHI NL - [N22000258	04/2010	377.93 -	986.30	- -	-	160.97
191	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263	04/2008	184.26 -	2,000.00	- -	-	985.42
192	ROHTAK-MEHAM HANSI - [N22000272	04/2012	287.00 -	576.18	- -	-	100.76
193	BHANUPALI-BILASPUR BERI NL - [N22000273	04/2008	1,046.88 -	2,966.99	- -	-	183.41
194	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276	04/2013	558.00 -	692.43	- -	-	24.09
195	SRINIVASA-PURA-MADANAPALLI NL - [N22000277	04/2013	296.00 -	466.65	- -	-	57.65
196	SHIMOGA-HARIHAR NL - [N22000278	04/2011	562.74 -	832.47	- -	-	47.93

(March 2015)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
197	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,743.00	- -	-	79.63
198	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29
199	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	329.97	- -	-	50.10
200	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	-	14.14
201	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00	- -	-	72.07
202	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	-	12.38
203	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]	04/1999	460.94 -	1,030.00	01/1999 -	-	123.46
204	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	800.00	01/1999 -	-	71.50
205	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	01/1999 -	-	53.96
206	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	679.27 -	1,111.99	- -	-	63.70
207	JHARSUGUDA-RENGALI DOUBLING - [N22000317]	03/2006	201.00 -	230.00	- -	-	14.43
208	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	826.57 -	1,143.60	- -	03/2018	38.35
209	DELANG-PURI DOUBLING - [N22000320]	03/2011	165.16 -	234.71	03/2015 -	03/2015	42.11
210	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10
211	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	209.00	12/2016 -	12/2016	40.49
	Total		82,753.31 -	209,968.62			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
212	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00 -	201.66	09/2008 -	03/2015	30.10
213	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	12/2015	28.93
214	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	06/2015	92.75
215	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	06/2015	80.68
216	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	06/2015	68.99
217	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	04/2010 -	01/2016	42.25
218	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	02/2017	2.29

(March 2015)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8
219	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098	12/2003	348.16 -	465.50	09/2007 -	06/2015	33.70
220	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	11/2015	106.50
	Total		2,934.62 -	4903.52			
	<u>SHIPPING AND PORTS</u>						
221	CONST. AND DEV. OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016	11/2007	1,228.00 -	1,460.00	12/2010 -	-	18.89
222	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	-	300.00
223	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST [N25000059	03/2007	245.67 -	373.22	04/2009 -	-	51.92
	Total		1,623.67 -	2,433.22			
	<u>STEEL</u>						
224	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067	10/2005	8,692.00 -	12,291.00	10/2009 -	05/2015	41.41
225	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	10/2016	42.39
	Total		9,035.00 -	12,779.40			
	<u>URBAN DEVELOPMENT</u>						
226	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00 -	11,609.00	06/2011 -	-	81.53
	Total		6,395.00 -	11,609.00			
	Grand Total		258,385.32	4,75,083.99			

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(March 2015)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	09/2016	62.57	72
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	22,462.00	12/2008 -	07/2015	70.54	79
	Total		16,663.00 -	28,139.00				
	<u>CIVIL AVIATION</u>							
3	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]	05/2010	335.61 -	388.53	05/2012 -	03/2015	15.77	34
	Total		335.61 -	388.53				
	<u>COAL</u>							
4	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	09/2015	478.50	30
5	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37	44
6	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	479.63	03/2013 -	03/2017	0.02	48
7	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,477.21	06/2009 -	04/2015	71.23	70
8	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,602.74	03/2012 -	04/2015	34.63	37
	Total		8,096.97 -	12,494.37				
	<u>PETROCHEMICALS</u>							
9	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	9,834.00	04/2012 -	06/2015	80.09	38
	Total		5,460.61 -	9,834.00				
	<u>PETROLEUM</u>							
10	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79	10/2014 -	10/2016	49.38	24
11	DEV OF G1 AND GS-15 (ONGCL) - [160100231]	04/2003	429.82 -	3,955.21	04/2006 -	06/2015	820.20	110
12	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) [N16000146]	02/2012	666.00 -	838.00	11/2015 -	11/2016	25.83	12

(March 2015)

Date of Commissioning (Month/Year)								
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
13	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]	01/2006	672.00 -	1,178.35	10/2011 -	10/2015	75.35	48
14	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]	01/2006	732.00 -	1,227.00	10/2011 -	10/2015	67.62	48
15	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	02/2016	37.72	11
16	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	10/2015	70.49	45
17	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	05/2016	29.42	14
18	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]	06/2007	3,248.78 -	6,000.00	08/2010 03/2012	05/2015	84.68	57
19	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]	12/2012	3,513.07 -	4,619.94	02/2016 -	04/2017	31.51	14
20	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00 -	34,555.00	11/2012 -	03/2015	16.05	28
	Total		43,272.46 -	58394.94				
	<u>POWER</u>							
21	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]	07/2012	296.87 -	363.73	12/2014 -	05/2015	22.52	5
22	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	346.79	08/2014 -	06/2015	16.63	10
23	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	07/1998	368.72 -	1,381.71	07/2006 02/2015	10/2016	274.73	123
24	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	994.85	07/2013 -	08/2015	136.30	25
25	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	721.81	09/2010 -	12/2015	51.10	63
26	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,487.49	08/2013 -	03/2016	159.15	31
27	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]	12/2011	901.77 -	1,025.28	08/2014 -	04/2015	13.70	8
28	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]	09/2005	1,061.38 -	1,929.15	09/2009 -	06/2016	81.76	81
29	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]	09/2011	1,366.34 -	1,606.38	12/2013 -	04/2015	17.57	16
30	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	07/2010 -	05/2018	79.77	94
31	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]	12/2011	1,746.65 -	2,228.71	08/2014 -	05/2015	27.60	9
32	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,159.07	09/2008 -	03/2016	21.34	90

(March 2015)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
33	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]	09/2010	2,074.86 -	2,348.37	03/2013 -	06/2015	13.18	27
34	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT [N18000042]	08/2008	2,491.58 -	3,745.08	07/2014 -	11/2018	50.31	52
35	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	4,676.34	12/2009 06/2016	03/2017	87.29	87
36	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C [N18000096]	03/2011	2,569.25 -	3,105.51	03/2014 -	06/2015	20.87	15
37	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	05/2018	29.14	62
38	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,497.72	01/2016 -	11/2016	50.95	10
39	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	7,531.72	09/2009 -	12/2018	92.16	111
40	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	6,749.18	09/2011 -	03/2017	54.25	66
41	KOLDAM HEP (NTPC) - [180100211]	10/2002	4,527.15 -	7,220.00	04/2009 -	06/2015	59.48	74
42	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	15,095.67	12/2009 -	03/2018	73.65	99
	Total		48,716.21 -	77039.72				
	<u>RAILWAYS</u>							
43	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	12/2009 -	06/2015	300.67	66
44	BANKURA - DAMODAR (GC) (SER) - [220100277]	03/1998	111.90 -	2,371.85	03/2005 12/2008	12/2019	2,019.62	177
45	ETAWAH-MAINPURI (NL),NCR - [220100318]	04/1997	120.00 -	245.39	12/2008 -	10/2015	104.49	82
46	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION [N22000162]	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44	21
47	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]	03/1996	155.74 164.36	883.00	02/2009 -	03/2015	466.97	73
48	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]	04/1986	158.77 274.56	608.02	03/1994 -	03/2015	282.96	252
49	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	272.39	03/2012 -	03/2016	59.20	48
50	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	194.07 -	335.00	06/2004 -	12/2015	72.62	138
51	KATAKHAL TO BHAIKABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41	39
52	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,428.00	06/2005 -	12/2019	385.76	174

(March 2015)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
53	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	03/2016	88.40	3
54	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,564.54	03/2010 -	03/2017	381.40	84
55	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30 -	1,544.40	03/1998 -	12/2019	299.79	261
56	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	03/2015	160.76	96
57	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]	04/2007	482.00 -	874.57	03/2013 -	09/2015	81.45	30
58	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	492.98 -	1,727.27	12/2010 -	03/2018	250.37	87
59	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	1,781.98	03/2004 -	03/2016	259.68	144
60	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,820.25	04/2014 -	03/2018	355.36	47
61	PATNA GANGA BRIDGE (NL), ECR - [220100308]	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76	98
62	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD [N22000213]	04/2012	632.68 -	816.55	03/2016 -	03/2018	29.06	24
63	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41	69
64	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	6,570.75	03/2011 -	03/2019	803.12	96
65	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	2,531.34	12/2008 -	03/2018	245.34	111
66	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	2,876.00	03/2014 -	03/2018	253.60	48
67	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	850.00 -	2,973.42	03/2015 -	03/2020	249.81	60
68	CONSTRUCTION OF NL FROM KUMARGHAT- AGARTALA [N22000194]	04/1999	895.00 -	1,242.25	03/2007 -	03/2016	38.80	108
69	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,190.00	12/2015 -	03/2020	212.81	51
70	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	06/2017	233.08	110
71	LUMDING-SILCHAR JIRIBAM, BADARPUR- BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	5,500.00	03/2009 -	03/2016	228.10	84
72	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60	193
73	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	6,821.29	03/2014 -	03/2019	28.70	60
	Total		23,474.35 -	80863.57				

(March 2015)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
74	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00 -	201.66	09/2008 -	03/2015	30.10	78
75	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	06/2015	80.68	79
76	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	06/2015	68.99	71
77	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	06/2015	92.75	74
78	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	04/2010 -	01/2016	42.25	69
79	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	02/2017	2.29	84
80	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	12/2015	28.93	82
81	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]	12/2003	348.16 -	465.50	09/2007 -	06/2015	33.70	93
82	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	11/2015	106.50	48
	Total		2,934.62 -	4903.52				
	<u>STEEL</u>							
83	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]	10/2005	8,692.00 -	12,291.00	10/2009 -	05/2015	41.41	67
	Total		8,692.00 -	12,291.00				
	Grand Total		157,645.83	2,84,348.65				

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	07/2015	13171	79
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	09/2016	3492	72
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	10/2017	11459	22
4	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	05/2018	12320	17

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
5	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	AAI	01/2009	01/2011	06/2016	309.46	65
6	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA)	AAI	05/2010	05/2012	03/2015	335.61	34
7	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	AAI	10/2012	03/2015	09/2015	217.6	6
8	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS	AAI	02/2010	03/2014	04/2015	344.28	13

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
9	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	NLC	10/2004	06/2009	04/2015	2030.78	70
10	CHURCHA ROUG(1.35MTY)	SECL	06/2008	03/2014	03/2016	462.35	24
11	BALRAM OCP EXTENSION,MCL 8.00 MTY	MCL	12/2007	03/2010	03/2017	172.08	84
12	TALABIRA OCP	MCL	03/2008	03/2016	03/2020	447.72	48
13	GOPAL PRASAD OCP (15MTY)	MCL	02/2008	03/2015	03/2021	395.87	72
14	KANIHA OCP, MCL, (10.0 MTY)	MCL	12/2007	03/2013	03/2017	457.77	48
15	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	03/2016	259.4	48
16	JHANJRA R-VI SEAM PSLW	ECL	11/2006	03/2011	03/2017	287.18	72
17	ADRIYALA SHAFT PROJECT	SCCL	12/2009	03/2013	09/2015	212.34	30
18	MAGADH OC 20 MTY (CCL)	CCL	08/2008	07/2012	03/2016	469.78	44
19	JALAGAM VENGALA RAO OCP-II	SCCL	07/2011	03/2015	03/2018	447.06	36
20	KISTARAM OCP	SCCL	11/2010	03/2015	03/2018	242.29	36

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project		DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
21	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2017	162.46	36
22	TAPIN OCP (2.5 MTY)	CCL	08/2008	03/2012	03/2016	264.68	48
23	PUKNADIH OCP (3.0 MTY)	CCL	07/2008	03/2013	03/2015	210.98	24
24	NORTH URIMARI OCP (3.0 MTY)	CCL	12/2007	03/2012	03/2017	179.87	60
25	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2016	163.51	60
26	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2009	03/2014	03/2016	321.5	24
27	MANUGURU OC-II EXTENSION PHASE-II	SCCL	03/2010	03/2012	03/2016	181.19	48
28	WIND POWER PROJECT, KAZHUNEERKULAM, TAMILNADU	NLC	04/2012	10/2014	06/2015	364.75	8
29	KALYANIKHANI OPENCAST PROJECT	SCCL	07/2012	07/2016	03/2017	417.33	8
30	RG OC -III EXTENSION (PHASE -II) PROJECT	SCCL	06/2012	06/2015	03/2016	365.01	9
31	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	04/2018	5907.11	28
32	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2016	418.97	48
33	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2016	178.44	24
34	JAGANNATHPOR OC	SECL	09/2008	03/2015	03/2017	152.43	24
35	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2017	479.53	48
36	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	03/2012	03/2017	207.28	60
37	RAJMAHAL OC EXP.	ECL	09/2009	03/2014	03/2016	153.82	24
38	KAKATIYA LONGWALL	SCCL	12/2008	12/2012	03/2017	453.63	51
39	TUTICORIN THERMAL POWER PROJECT-2X500 MW	NLC	05/2008	03/2012	04/2015	4904.54	37
40	KULDA OCP (MAHANADI COALFIELDS LTD)	MCL	01/2005	03/2010	03/2017	302.96	84
41	GEVRA EXPANSION OCP (SECL) (25-35) MTY	SECL	06/2010	03/2014	03/2016	2675.67	24
42	DIPKA EXPANSION OCP (SECL) (20-25) MTY	SECL	12/2009	03/2014	03/2016	1943.66	24
43	BLOCK-B OCP NCL (3.5 MTY)	NCL	06/2011	03/2015	03/2016	746.04	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project		DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
44	KRISHNASHILA (NCL) (4MTY)	NCL	06/2011	03/2013	03/2016	789.88	36
45	ASHOK EXPN OCP CCL (10 MTY)	CCL	12/2007	03/2011	03/2017	471.66	72

PETROCHEMICALS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
46	ASSAM GAS CRACKER PROJECT	BCPL	04/2006	04/2012	06/2015	5460.61	38

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
47	DEV OF G1 AND GS-15 (ONGCL)	ONGC	04/2003	04/2006	06/2015	429.82	110
48	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA	ONGC	07/2008	08/2012	03/2015	288.04	31
49	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	11/2017	202.94	46
50	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV)	ONGC	11/2010	08/2013	05/2015	331.2	21
51	ANKLESWAR REDEVELOPMENT	ONGC	11/2010	12/2014	12/2018	2189.63	48
52	MEHESANA REDEVELOPMENT PROJECT	ONGC	11/2010	04/2015	12/2017	3823	32
53	AHMEDABAD REDEVELOPMENT PROJECT	ONGC	11/2010	12/2014	12/2017	1916.1	36
54	102 MW WIND POWER PROJECT	ONGC	07/2010	06/2012	03/2015	1106	33
55	CONSTRUCTION OF 6 ETPS	ONGC	03/2009	09/2012	10/2015	317.64	37
56	DEVELOPMENT OF W0-16 CLUSTER FIELDS	ONGC	06/2010	01/2014	12/2015	2523	23
57	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV)	ONGC	01/2010	03/2013	06/2016	723.64	39
58	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	10/2016	309.81	24
59	MOUNDED BULLET PROJECT AT CPCL	CPCL	12/2012	12/2014	07/2015	279	7
60	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	11/2016	666	12
61	IOR OF B-173A FIELD	ONGC	01/2012	03/2014	04/2015	352.49	13
62	PIPELINE REPLACEMENT PROJECT-3	ONGC	04/2012	05/2014	05/2015	2547.26	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project		DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
63	DEVELOPMENT OF C-26 CLUSTER FIELDS	ONGC	03/2012	05/2014	03/2016	2592.17	22
64	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	05/2016	2059.63	14
65	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT	GAIL	06/2009	12/2012	06/2015	2915	30
66	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	03/2015	861.79	22
67	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND)	IOCL	04/2011	05/2015	12/2015	191.96	7
68	IMPROVED OIL RECOVERY OF B-173A FIELD	ONGC	01/2012	03/2014	03/2016	352.49	24
69	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1)	ONGC	10/2013	10/2014	10/2015	429.06	12
70	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS	ONGC	03/2013	05/2016	04/2018	2913.1	23
71	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE	ONGC	04/2013	04/2015	05/2017	284.82	25
72	LPG TERMINAL AT KOCHI	IOCL	12/2012	01/2016	04/2017	607.06	15
73	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	10/2015	993	45
74	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG	OIL	04/2010	06/2012	11/2015	270	41
75	INTEGRATED DEVELOPMENT OF BASSEIN FIELD	ONGC	12/2012	02/2016	04/2017	3513.07	14
76	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	ISPRL	01/2006	10/2011	10/2015	732	48
77	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG	ISPRL	01/2006	10/2011	10/2015	672	48
78	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	02/2016	871.35	11
79	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH)	GAIL	12/2009	06/2011	07/2015	463.32	49
80	PARADIP REFINERY PROJECT	IOCL	02/2009	11/2012	03/2015	29777	28
81	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I	GAIL	07/2009	01/2013	02/2019	7596.18	73
82	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	ONGC	06/2007	09/2011	12/2015	736.65	51
83	PARADIP-RAIPUR- RANCHI PIPELINE	IOCL	08/2009	09/2012	03/2016	1793	42
84	ASSAM RENEWAL PROJECT FOR GROUP A	ONGC	03/2009	03/2013	03/2016	2465.15	36
85	DEVELOPMENT OF B-193 CLUSTER FIELDS	ONGC	06/2007	08/2010	05/2015	3248.78	57

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
86	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2018	3919.59	111
87	BARH STPP STAGE -II	NTPC	02/2008	10/2013	03/2015	7341.04	17
88	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	03/2016	573.99	31
89	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	07/2014	11/2018	2491.58	52
90	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	03/2017	4375.35	66
91	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	12/2015	477.69	63
92	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	11/2016	3642.04	10
93	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	05/2018	2978.48	62
94	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	07/2010	05/2018	1657	94
95	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID	PGCIL	09/2012	03/2015	12/2015	1508.74	9
96	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B	PGCIL	03/2011	11/2013	06/2015	1585.12	19
97	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A	PGCIL	05/2010	01/2013	06/2015	250.03	29
98	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C	PGCIL	03/2011	03/2014	06/2015	2569.25	15
99	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI	PGCIL	08/2010	04/2013	03/2016	1677.57	35
100	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI	PGCIL	07/2010	07/2013	12/2015	752.64	29
101	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B	PGCIL	12/2010	12/2013	09/2015	2743.19	21
102	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A	PGCIL	09/2010	03/2013	06/2015	2074.86	27
103	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME	PGCIL	03/2010	11/2012	12/2015	965.58	37
104	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP)	PGCIL	12/2009	08/2012	03/2016	1216.83	43
105	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED	PGCIL	12/2011	02/2014	09/2015	552.44	19
106	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2	PGCIL	12/2011	08/2014	06/2015	2422.66	10
107	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH	PGCIL	11/2011	07/2014	05/2015	2127.51	10
108	SYTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	09/2015	487.49	15

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
109	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH	PGCIL	09/2011	12/2013	04/2015	1366.34	16
110	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1	PGCIL	10/2011	11/2013	12/2015	558.26	25
111	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND- BARATH POWER(MADRAS) LIMITED L	PGCIL	09/2011	09/2014	06/2015	1940.13	9
112	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH	PGCIL	05/2011	05/2014	03/2015	1961.87	10
113	EASTERN REGION STRENGTHENING SCHEME - III	PGCIL	07/2010	11/2012	03/2016	1272.8	40
114	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	03/2016	2144	39
115	TRANSM SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B	PGCIL	04/2010	01/2015	12/2015	4404.57	11
116	TRANSMISSION SYSTEM OF VINDHUACHAL - IV AND RIHAND -III GEN. PROJ.	PGCIL	03/2010	11/2012	07/2015	4672.99	32
117	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	08/2015	421.01	25
118	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	03/2016	11130.19	31
119	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	03/2016	4824.12	41
120	NORTHERN REGION SYSTEM STRENGHTENING SCHEME-XIX	PGCIL	02/2009	02/2012	03/2016	410.29	49
121	NORTHERN REGION SYSTEM STRENGHTENING SCHEME-XVIII	PGCIL	02/2009	11/2011	03/2016	509.66	52
122	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS	PGCIL	12/2011	08/2014	04/2015	901.77	8
123	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	03/2012	06/2015	12/2015	9569.76	6
124	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION)	PGCIL	03/2012	03/2014	03/2015	213.78	12
125	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION	PGCIL	03/2012	09/2014	06/2016	198.63	21
126	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B	PGCIL	02/2012	10/2014	04/2015	1927.16	6
127	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	10/2016	368.72	123
128	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	01/2012	01/2015	12/2015	1422.85	11
129	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	05/2015	1746.65	9
130	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	06/2015	297.33	10
131	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI	PGCIL	06/2012	06/2015	12/2015	1909.24	6

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project		DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
132	SOLAPUR STPP	NTPC	03/2012	11/2016	08/2017	9395.18	9
133	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID	PGCIL	06/2012	11/2014	06/2015	1263.26	7
134	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B	PGCIL	02/2012	10/2014	06/2015	3201.44	8
135	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV	PGCIL	11/2011	11/2014	12/2015	723.63	13
136	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	03/2017	2496.9	87
137	BARH STPP(3X660MW) NTPC	NTPC	02/2005	12/2009	03/2018	8692.97	99
138	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	NHPC	09/2005	09/2009	06/2016	1061.38	81
139	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	09/2008	03/2016	1779.29	90
140	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL)	PGCIL	03/2005	12/2007	12/2015	1007.16	96
141	KOLDAM HEP (NTPC)	NTPC	10/2002	04/2009	06/2015	4527.15	74

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
142	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR)	NCR	04/1986	03/1994	03/2015	158.77	252
143	RANCHI-LOHARDAGA(GC),SER	SER	04/1997	06/2004	12/2015	194.07	138
144	ETAWAH-MAINPURI (NL),NCR	NCR	04/1997	12/2008	10/2015	120	82
145	PATNA GANGA BRIDGE (NL), ECR	ECR	04/2001	10/2007	12/2015	624.47	98
146	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2019	727.56	96
147	BANKURA - DAMODAR (GC) (SER)	SER	03/1998	03/2005	12/2019	111.9	177
148	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	NFR	04/2000	12/2008	03/2018	733	111
149	KATIHAR - JOGBANI (GC)(NEFR)	NFR	09/2001	12/2010	03/2018	492.98	87
150	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	12/2009	06/2015	108	66
151	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	03/2015	393.46	96
152	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	SWR	04/2007	03/2013	09/2015	482	30
153	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	51

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project		DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
154	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2018	619.34	47
155	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2018	813.34	48
156	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	12/2019	293.97	174
157	ELECTRIFICATION OF KHURJA-MEERUT- SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	03/2016	171.1	48
158	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	MRTP	04/2008	03/2014	03/2019	5300	60
159	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	03/2017	325	84
160	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	12/2015	687.2	69
161	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE	MRTP	04/2012	04/2016	03/2017	714.1	11
162	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	MRTP	04/2012	03/2016	03/2018	632.68	24
163	CONSTRUCTION OF NL FROM KUMARGHAT- AGARTALA	NFR	04/1999	03/2007	03/2016	895	108
164	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION	SER	04/2010	03/2015	12/2016	149.9	21
165	LUMDING-SILCHAR JIRIBAM, BADARPUR- BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	03/2016	1676.31	84
166	KATAKHAL TO BHAIRABI	NFR	04/1998	12/2012	03/2016	227.9	39
167	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2020	850	60
168	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	ER	04/1999	12/2012	09/2015	207.52	33
169	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	03/2016	2298.42	24
170	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2018	2500	193
171	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	03/1998	12/2019	386.3	261
172	NANDYAL-YERRAGUNTALA(NL), SCR	SCR	03/1996	02/2009	03/2015	155.74	73
173	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2017	1500	110
174	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	MRTP	03/1996	03/2004	03/2016	495.44	144

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
175	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	NHAI	12/2003	09/2007	03/2015	157.47	90
176	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	06/2015	155.04	79
177	BIJNI TO ASSAM WB BORDER (NH- 31.C)(1)(NHAI)	NHAI	12/2003	06/2008	08/2015	195	86
178	HARANGAJO TO MAIBANG, KM 164.08- 190.587 NH-54	NHAI	12/2003	09/2007	12/2015	212	99
179	DHARAMTUL TO SONAPUR (AS-19)	NHAI	12/2003	06/2008	03/2015	200	81
180	DHARAMTUL TO SONAPUR, KM 205-183 (AS- 20)	NHAI	12/2003	05/2008	06/2015	160	85
181	NALBARI T BIJNI (AS-7)	NHAI	12/2003	04/2008	12/2015	208	92
182	NALBARI TO BIJNI (AS-6)	NHAI	12/2003	06/2008	04/2015	225	82
183	GUWAHATI TO NALBARI (AS-5)	NHAI	12/2003	04/2008	03/2015	198.16	83
184	SONAPUR TO GUWAHTI (AS-3)	NHAI	12/2003	03/2008	03/2015	245	84
185	NAGAON TO DHARAMTUL (AS-2)	NHAI	12/2003	06/2008	03/2015	264.72	81
186	GUWHATI TO NALBARI (AS-4)	NHAI	12/2003	04/2008	04/2015	175.96	84
187	CHENGAPALLI TO COIMBATORE BYPASS KM- 102.035-144.740 KM	NHAI	09/2010	03/2013	12/2015	852	33
188	HAZARIBAGH-RANCHI	NHAI	08/2010	01/2013	03/2015	625.07	26
189	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4	NHAI	09/2010	09/2013	11/2016	1655	38
190	INDORE-JHABUA-GUJRAT/MP	NHAI	10/2010	04/2013	12/2015	1175	32
191	JAIPUR-TONK-DEOLI	NHAI	06/2010	12/2012	03/2015	792.06	27
192	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	11/2015	1108	48
193	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15)	NHAI	05/2009	10/2011	06/2015	572.3	44
194	CHENNAI-TADA(SIX LANE)	NHAI	04/2009	10/2011	06/2016	353.37	56
195	KISHANGARH-AJMER-BEAWER	NHAI	11/2009	05/2012	09/2015	795	40
196	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	NHAI	09/2011	12/2013	05/2015	1250	17
197	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00	NHAI	06/2011	12/2013	03/2015	535	15

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
198	GHAZIABAD-ALIGARH NH-91	NHAI	02/2011	08/2013	06/2015	1141	22
199	ROHTAK-BAWAL	NHAI	05/2011	11/2013	06/2015	650	19
200	PATNA-MUZZAFFARPUR	NHAI	08/2010	02/2013	03/2015	671.3	25
201	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	NHAI	07/2010	07/2013	09/2015	1813.76	26
202	NASHRI- CHANANI	NHAI	05/2011	06/2015	06/2016	2159	12
203	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	NHAI	07/2010	07/2015	06/2016	1987	11
204	INDORE-DEWAS(NH-3)	NHAI	11/2010	05/2013	12/2015	325	31
205	BHOPAL-SANCHI	NHAI	10/2011	01/2013	12/2015	209	35
206	4-LANING OF BARHI-HAZARIBAGH	NHAI	02/2012	02/2014	09/2015	398	19
207	SRINAGAR TO BANIHAL	NHAI	06/2011	06/2014	12/2015	1100.7	18
208	2 LANNING OF MUZAFFARPUR - SONBARSA	NHAI	05/2011	11/2013	05/2015	511.54	18
209	4-LANNING OF CHAPRA-HAJIPUR	NHAI	01/2011	07/2013	12/2015	575	29
210	2-LANNING WITH PS MOTIHARI-RAXAUL	NHAI	10/2011	04/2014	03/2015	375.09	11
211	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	NHAI	09/2011	03/2014	11/2015	574	20
212	2-LANNING WITH PS KHAGARIA-PURNEA	NHAI	05/2011	02/2014	10/2015	664	20
213	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	NHAI	11/2011	05/2014	12/2015	1535	19
214	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI	NHAI	07/2012	07/2014	03/2015	356.4	8
215	KRISHNANAGAR-BERHAMPUR	NHAI	02/2012	07/2014	02/2017	702.16	31
216	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	NHAI	07/2012	01/2014	12/2015	291.36	23
217	6-LANING OF DHANKUNI-KHARAGPUR SECTION	NHAI	04/2012	09/2014	12/2015	1396.18	15
218	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	NHAI	12/2011	06/2014	12/2015	1047	18
219	4-LANING OF RAIGANJ-DALKOLA	NHAI	02/2011	08/2013	05/2017	580.43	45
220	4-LANING OF BRAHAMPUR-FARAKA	NHAI	02/2011	08/2013	07/2017	998.79	47

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project		DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
221	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	08/2013	08/2016	1078.84	36
222	MUZAFFARNAGAR-HARIDWAR	NHAI	09/2011	03/2013	12/2015	754	33
223	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	NHAI	05/2013	02/2014	08/2016	1348.2	30
224	BARSAT-KRISHNANAGAR	NHAI	08/2012	02/2015	12/2017	867	34
225	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8	NHAI	06/2013	11/2015	03/2017	1287.95	16
226	REENGUS SIKAR	NHAI	03/2012	09/2014	03/2015	333.51	6
227	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6	NHAI	03/2012	09/2014	03/2015	828	6
228	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	04/2016	1928.22	12
229	2 LANING WITH PS KANPUR KABRAI	NHAI	01/2013	07/2014	03/2015	373.47	8
230	FOUR LANING OF ORISSA CHATTISHGARH BORDER	NHAI	02/2013	08/2015	02/2016	1232	6
231	PANVEL-INDAPUR	NHAI	12/2011	06/2014	12/2015	942.69	18
232	RANCHI-RARGA-JAMSETHPUR	NHAI	12/2012	06/2015	06/2016	1479	12
233	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION	NHAI	04/2011	10/2013	11/2015	682	25
234	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHTH 170 KM)	NHAI	04/2012	04/2014	07/2015	624	15
235	HARIDWAR-DEHRADUN (APPROVED LENGTH 69)	NHAI	11/2011	10/2013	12/2015	478	26
236	BAREILY-SITAPUR (NH-24)	NHAI	03/2011	09/2013	12/2015	1046	27
237	BEAWAR-PALI-PINDWARA	NHAI	12/2011	06/2014	11/2015	2388	17
238	JAIPUR-REENGUS	NHAI	08/2010	02/2013	03/2015	267.81	25
239	PANIKHOLI-RIMOLI	NHAI	03/2012	09/2014	06/2016	1410	21
240	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER	NHAI	11/2011	05/2014	03/2015	909	10
241	BHUBANESWAR TO PURI	NHAI	03/2011	08/2013	03/2015	500.29	19
242	NIROLI-ROXY-RAJAMUNDA	NHAI	07/2011	01/2014	12/2016	586	35
243	PUNE-SHOLAPUR, PKG-II	NHAI	09/2011	01/2014	03/2015	835	14

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
244	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	04/2017	2848 37
245	JORBAT - BARAPANI	NHAI	01/2011	01/2014	03/2015	536 14
246	SAMAIKHIALI - GANDHIDHAM	NHAI	09/2010	03/2013	12/2015	805.39 33
247	TIRUPATI - TIRUTHANI - CHENNAI	NHAI	04/2011	10/2013	03/2016	571 29
248	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI	NHAI	09/2011	08/2013	12/2015	485 28
249	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS	NHAI	05/2010	05/2013	05/2015	374 24
250	KANDLA - MUNDRA PORT	NHAI	01/2011	07/2013	06/2015	953.88 23
251	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	NHAI	06/2011	06/2013	03/2015	600 21
252	PUNE-SATARA(NH-4)	NHAI	10/2010	03/2013	12/2015	1724.55 33
253	4 LANING OF NAGPUR-BETUL	NHAI	02/2011	08/2014	03/2015	2498.76 7
254	MURADABAD-BAREILY	NHAI	04/2010	06/2013	03/2015	1267 21
255	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER	NHAI	03/2011	09/2013	12/2016	359 39
256	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM)	NHAI	02/2011	11/2012	12/2016	193.45 49
257	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM)	NHAI	02/2010	08/2012	03/2016	617 43
258	DEOLI-KOTA	NHAI	01/2011	07/2013	04/2016	593 33
259	CUDDAPAH-MYDUKUR-KURN00L KM-167.750-356.502 KM	NHAI	11/2010	05/2013	12/2015	1585 31
260	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	NHAI	03/2010	09/2012	11/2015	1509.1 38
261	DELHI/ HARYANA BORDER TO ROHTAK	NHAI	04/2007	05/2010	06/2015	486 61
262	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	NHAI	12/2003	09/2010	12/2015	232.45 63
263	AGRA-BYPASS(NS-1/UP-1), NH-2,3	NHAI	12/2003	09/2007	06/2015	348.16 93
264	GWALI0R-JHANSI, NH-75	NHAI	12/2003	12/2009	04/2015	604 64
265	CHAMBAL BRIDGE, NH-76 (RJ-5)	NHAI	12/2003	02/2010	02/2017	275 84
266	BRAHMPUTRA BRIDGE,NH N0-31	NHAI	12/2003	04/2010	01/2016	217.61 69

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project		DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
267	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	06/2015	196	71
268	KOTA BYPASS,RJ-4, NH-76 (NHAI)	NHAI	12/2003	10/2008	05/2015	275	79
269	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	NHAI	12/2003	09/2008	06/2015	332.94	81
270	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	NHAI	12/2003	06/2008	09/2015	237.8	87
271	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	NHAI	12/2003	04/2009	06/2015	200	74
272	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	NHAI	12/2003	11/2008	06/2015	167.64	79
273	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06	NHAI	12/2003	09/2008	03/2015	155	78
274	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C	NHAI	12/2003	06/2005	12/2015	230	126
275	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	06/2015	199.81	74
276	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	NHAI	12/2003	02/2009	12/2015	280	82

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
277	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	RINL	10/2005	10/2009	05/2015	8692	67
278	BAILADILA IRON ORE PROJECT DEPOSIT-11B (NMDC)	NMDC	01/2007	12/2011	03/2015	607.17	39
279	AUGMENTATION OF IRON ORE STORAGE IN RMHP	RINL	07/2007	09/2009	06/2015	480	69
280	EXPANSION OF BOKARO STEEL PLANT	SAIL	05/2010	12/2011	05/2015	6325	41
281	EXPANSION OF BHILAI STEEL PLANT	SAIL	08/2010	03/2013	09/2015	17265	30
282	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC)	NMDC	04/2011	04/2013	06/2015	572	26
283	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC)	NMDC	02/2011	05/2013	08/2015	898.55	27
284	EXPANSION OF DURGAPUR STEEL PLANT	SAIL	08/2010	12/2012	05/2015	2875	29
285	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES	SAIL	11/2011	11/2013	06/2015	254.55	19
286	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES	SAIL	12/2011	10/2013	08/2015	187.33	22
287	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH	SAIL	07/2012	08/2014	06/2015	332.65	10
288	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA	SAIL	06/2012	12/2014	08/2015	237.09	8

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
289	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP	SAIL	10/2012	09/2014	06/2015	160.48	9
290	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	12/2016	15525	19
291	CAPTIVE POWER PLANT - 2	RINL	02/2011	09/2013	05/2015	677	20
292	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS	RINL	07/2011	07/2015	03/2016	877.73	8
293	SMS-1 CONVERTERS REVAMPING	RINL	05/2012	07/2015	03/2017	404.16	20

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
294	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G	BSNL	06/2007	01/2009	03/2015	336.81	74
295	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS	BSNL	10/2009	10/2010	09/2015	384	59

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
296	DELHI MRTS PHASE-III	DMRCL	09/2011	03/2016	12/2016	38585	9
297	FARIDABAD EXTENSION	DMRCL	09/2011	09/2014	05/2015	2494	8
298	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL	CPWD	12/2012	12/2014	12/2016	188.87	24
299	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA	CPWD	01/2009	06/2012	06/2015	225.81	36
300	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	CPWD	02/2014	09/2015	07/2016	156.57	10
301	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	CPWD	11/2012	11/2014	10/2015	270.83	11
302	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB	CPWD	11/2012	02/2015	08/2015	238.43	6
303	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI	CPWD	05/2009	05/2013	11/2015	261.85	30
304	C/O MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB	CPWD	08/2005	08/2007	03/2015	191.24	91
305	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA	CPWD	06/2010	03/2012	04/2015	205	37
306	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI	CPWD	05/2012	12/2014	04/2016	405.01	16
307	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	CPWD	07/2012	08/2014	06/2017	884.3	34

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project		DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
308	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	08/2016	14600	8
309	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	01/2015	12/2015	23136	11

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	5677	2185
2	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	13171	22462	9291

COAL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
3	TUTICORIN THERMAL POWER PROJECT- 2X500 MW	NLC	05/2008	03/2012	4904.54	6602.74	1698.2
4	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	NLC	10/2004	06/2009	2030.78	3477.21	1446.43
5	ADRIYALA SHAFT PROJECT	SCCL	12/2009	03/2013	212.34	1228.39	1016.05
6	MAGADH OC 20 MTY (CCL)	CCL	08/2008	07/2012	469.78	706.4	236.62

PETROCHEMICALS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
7	ASSAM GAS CRACKER PROJECT	BCPL	04/2006	04/2012	5460.61	9834	4373.39

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
8	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG	ISPRL	01/2006	10/2011	672	1178.35	506.35
9	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	871.35	1200	328.65
10	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	993	1693	700
11	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	666	838	172
12	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	ISPRL	01/2006	10/2011	732	1227	495
13	INTEGRATED REFINERY EXPANSION PROJECT	BPCL	03/2012	05/2016	14225	16504	2279
14	INTEGRATED DEVELOPMENT OF BASSEIN FIELD	ONGC	12/2012	02/2016	3513.07	4619.94	1106.87
15	DEVELOPMENT OF B-193 CLUSTER FIELDS	ONGC	06/2007	08/2010	3248.78	6000	2751.22
16	DEV OF G1 AND GS-15 (ONGCL)	ONGC	04/2003	04/2006	429.82	3955.21	3525.39
17	DEVELOPMENT OF CLUSTER-7 FIELDS	ONGC	03/2010	03/2013	4550.4	6638.94	2088.54
18	REWARI KANPUR PIPELINE PROJECT	HPCL	02/2012	11/2015	1210.64	1446.34	235.7
19	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	309.81	462.79	152.98

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
20	PARADIP REFINERY PROJECT	IOCL	02/2009	11/2012	29777	34555	4778
21	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	2059.63	2665.65	606.02
22	MH NORTH REDEVELOPMENT PHASE III	ONGC	06/2014	05/2017	5706.47	5813.25	106.78
POWER							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
23	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	573.99	1487.49	913.5
24	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	2496.9	4676.34	2179.44
25	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	15300	9014.67
26	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS	PGCIL	12/2011	08/2014	901.77	1025.28	123.51
27	KOLDAM HEP (NTPC)	NTPC	10/2002	04/2009	4527.15	7220	2692.85
28	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	3642.04	5497.72	1855.68
29	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	1746.65	2228.71	482.06
30	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C	PGCIL	03/2011	03/2014	2569.25	3105.51	536.26
31	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH	PGCIL	09/2011	12/2013	1366.34	1606.38	240.04
32	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	NHPC	09/2005	09/2009	1061.38	1929.15	867.77
33	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	421.01	994.85	573.84
34	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	09/2008	1779.29	2159.07	379.78
35	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A	PGCIL	09/2010	03/2013	2074.86	2348.37	273.51
36	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	368.72	1381.71	1012.99
37	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	477.69	721.81	244.12
38	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	07/2010	1657	2978.86	1321.86
39	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	3846.3	867.82
40	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	07/2014	2491.58	3745.08	1253.5

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
41	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	7531.72	3612.13
42	BARH STPP(3X660MW) NTPC	NTPC	02/2005	12/2009	8692.97	15095.67	6402.7
43	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	4375.35	6749.18	2373.83

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
44	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	03/2008	743	1117.11	374.11
45	RAICHUR-GUNTAKAL(DL)(SCR)	RVNL	04/2003	12/2007	136.62	289.93	153.31
46	LUMDING-HOJAI PATCH DOUBLING PROJECT	NFR	04/2012	N.A.	246.07	364.06	117.99
47	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	1676.31	5500	3823.69
48	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	N.A.	200	496.24	296.24
49	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	332.92	477.88	144.96
50	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	N.A.	300	827.73	527.73
51	KISHANGANJ JALALGARH, NL, NEFR	NFR	04/2008	N.A.	282.92	565.13	282.21
52	SAKRI-HASANPUR ROAD (NL)	ECOR	04/1999	N.A.	175.69	325	149.31
53	HAJIPUR-RAMDAYALUNAGAR DOUBLING	ECR	04/2013	N.A.	213.01	367.17	154.16
54	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	1500	4996.19	3496.19
55	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	NFR	01/2004	N.A.	915.7	3700	2784.3
56	KATAKHAL TO BHAIRABI	NFR	04/1998	12/2012	227.9	331.4	103.5
57	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	N.A.	312.12	453.1	140.98
58	CHHINDWARA - NAGPUR (GC)(SECR)	SECR	04/2005	N.A.	383.79	1101.16	717.37
59	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	687.2	800	112.8
60	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2012	603.04	1421.25	818.21
61	ANGAMALI-SABARIMALA (N.L.)(SR)	SR	10/1998	N.A.	550	1566	1016
62	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR	SWR	02/1997	N.A.	295	1289.92	994.92

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
63	HUBLI-ANKOLA(NL),SWR	SWR	04/1997	N.A.	227	2135	1908
64	GULBARGA-BIDAR, SCR(NL)	SCR	02/1998	N.A.	242.42	844	601.58
65	BANGLORE - SATYAMANGALAM (NL)(SWR)	SWR	04/1996	N.A.	138	1382.78	1244.78
66	MUNIRABAD (GINGERA) -RAICHUR NL	SWR	04/2007	N.A.	179.65	1350.91	1171.26
67	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	SR	04/1999	N.A.	198.68	556.64	357.96
68	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	SR	04/1998	N.A.	271.24	520	248.76
69	ERODE-PALANI	SR	04/2008	N.A.	288.57	603.22	314.65
70	MADURAI-BODINAYAKKANUR	SR	04/2008	N.A.	164.41	450	285.59
71	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	SR	04/2007	N.A.	247	951.24	704.24
72	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI	SR	04/1999	01/1999	460.94	1030	569.06
73	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	4190	2850.52
74	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR	NWR	04/2013	N.A.	456	855.16	399.16
75	RATANGARH-SARDARSAHAR (MM OF SADULPUR- BIKANER AND RATANGARH-DEGANA GC)	NWR	04/2010	N.A.	739.65	872.22	132.57
76	MM FROM PANSKURA-GHATAL NL	SER	04/2011	01/1999	276.69	426	149.31
77	KANPUR-KASGANJ-MATHURA(GC),NER	NER	03/1997	N.A.	677.97	1651.54	973.57
78	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	12/2009	108	432.72	324.72
79	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR- NAUTANWA GC (NER)	NER	04/1997	N.A.	863.23	1072.51	209.28
80	ETAWAH-MAINPURI (NL),NCR	NCR	04/1997	12/2008	120	245.39	125.39
81	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	325	1564.54	1239.54
82	ELECTRIFICATION OF KHURJA-MEERUT- SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	171.1	272.39	101.29
83	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	813.34	2876	2062.66
84	CONSTRUCTION OF NL FROM KUMARGHAT- AGARTALA	NFR	04/1999	03/2007	895	1242.25	347.25
85	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-	NFR	04/1999	N.A.	523.17	1653.55	1130.38

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
	NAXAL& RAJABHATKHOWA-JAI						
86	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI	SR	04/2011	N.A.	601.43	800	198.57
87	PEN ROHA DOUBLING	CR	04/2007	N.A.	98.74	203	104.26
88	PANVEL PEN DOUBLING	CR	04/2006	N.A.	96.16	260.16	164
89	AKOLA-KHANDWA GC AKOLA-AKOT	SCR	04/2008	N.A.	184.26	2000	1815.74
90	SRINIVASA-PURA-MADANAPALLI NL	SWR	04/2013	N.A.	296	466.65	170.65
91	RAYADURGA-TUMKUR NL	SWR	04/2007	N.A.	970.34	1743	772.66
92	MM FROM BURAMARA-CHAKULIA	SER	04/2008	01/1999	466.48	800	333.52
93	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR	NFR	04/1983	N.A.	36.8	1336.57	1299.77
94	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	SCR	12/1994	N.A.	124.43	925.3	800.87
95	MACHERLA-NALGONDA(NL)(SCR)	SCR	07/1998	07/2008	125	480	355
96	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	N.A.	378.56	791.59	413.03
97	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	M RTP	04/2012	03/2016	632.68	816.55	183.87
98	HARIDWAR-LAKSAR	NR	04/2012	N.A.	219.83	329.97	110.14
99	RANCHI-LOHARDAGA(GC),SER	SER	04/1997	06/2004	194.07	335	140.93
100	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	12/2015	309.44	583	273.56
101	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	N.A.	258.2	365	106.8
102	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL	RVNL	04/1995	12/2012	304	968.6	664.6
103	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	N.A.	826.57	1143.6	317.03
104	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	NCR	04/1986	03/1994	158.77	608.02	449.25
105	VIRAMGAM-BHILDI(WR),GC	WR	04/1990	N.A.	155.66	548.01	392.35
106	CALICUT-MANGALORE (DL) (SR)	SR	02/1996	N.A.	240	579.37	339.37
107	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	03/1998	386.3	1544.4	1158.1
108	NANGALDAM-TALWARA(NL),NR	NR	03/1981	07/2012	450	2100	1650

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
109	MUNEERABAD-MAHABOBNAGAR(NL), SCR	SCR	04/1997	N.A.	218.24	645	426.76
110	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	1630.97	1383.31
111	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	NR	03/2002	06/2007	625.3	847.75	222.45
112	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	SR	03/1998	N.A.	280	1122	842
113	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	NFR	04/2000	12/2008	733	2531.34	1798.34
114	GADWAL - RAICHUR (NL), SCR	SCR	04/1998	02/2011	92.63	270	177.37
115	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	NFR	12/2006	03/2011	170	485	315
116	CHHAPRA-BALLIA UP	NER	03/2013	N.A.	295	494.92	199.92
117	RATLAM-DUNGARPUR VIA BANSWARA (NL)	NWR	04/2011	N.A.	2082.75	3500	1417.25
118	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	1176.09	3845.6	2669.51
119	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR	NCR	04/2010	02/2019	622.41	2030.5	1408.09
120	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	N.A.	553.63	1009	455.37
121	CHENNAI-CUDDALORE VIA MAMALLAPURAM	SR	04/2008	N.A.	523.52	1200	676.48
122	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	SR	04/2008	N.A.	822.39	1280.83	458.44
123	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	N.A.	242.22	679.57	437.35
124	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	394.28	152.76
125	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	N.A.	165.82	435.58	269.76
126	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	393.46	1026	632.54
127	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	M RTP	03/2000	12/2006	1049.69	3404.92	2355.23
128	BANKURA - DAMODAR (GC) (SER)	SER	03/1998	03/2005	111.9	2371.85	2259.95
129	TAMLUK DIGHA,LINE DOUBLING (SER)	SER	03/1984	06/2005	293.97	1428	1134.03
130	BOWAICHANDI-ARAMBAGH	SER	04/2010	N.A.	267.37	434	166.63
131	BHADUTOLA-JHARGRAM VIA LALGARH (NL)	SER	04/2011	N.A.	289.64	760	470.36

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
132	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	NFR	04/2010	N.A.	221.42	563.13	341.71
133	NEW COOCHBEHAR TO SAMUKTALA	NFR	04/2011	N.A.	209.77	441.45	231.68
134	AGARTALA-AKHAURA NL	NFR	04/2012	N.A.	252	886.65	634.65
135	KARUR-SALEM(NL), SR	SR	02/1997	N.A.	155.55	800	644.45
136	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	09/1995	N.A.	100	980	880
137	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	SR	09/2007	N.A.	404.19	1383.45	979.26
138	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	SR	09/2006	N.A.	343.17	914.98	571.81
139	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	SR	09/2006	N.A.	125	490	365
140	TIDIVANAM-NAGARI (NL)	SR	09/2006	N.A.	456	1080	624
141	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	SR	04/2013	N.A.	839	1500	661
142	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	N.A.	470.21	1995.25	1525.04
143	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	N.A.	301.64	1185.64	884
144	RAJATGARH-BARANG(LD),ECOR	RVNL	04/1999	02/2009	166.16	288	121.84
145	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	183.23	818.29	635.06
146	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	133.41	276	142.59
147	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	N.A.	679.27	1111.99	432.72
148	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	850	2973.42	2123.42
149	DIMAPUR-TIZIT NL	NFR	04/2013	N.A.	4274	4487.7	213.7
150	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	619.34	2820.25	2200.91
151	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	N.A.	4083.02	5307.9	1224.88
152	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	727.56	6570.75	5843.19
153	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	495.44	1781.98	1286.54
154	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	N.A.	514.68	2820	2305.32

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
155	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	5300	6821.29	1521.29
156	WARDHA-NANDED MAHARASHTRA	CR	04/2008	N.A.	499.3	2501.05	2001.75
157	RAMGANJ MUNDI-BHOPAL (NL), WCR	WCR	04/2001	N.A.	470.92	1225.9	754.98
158	BAGALKOT-KUDACHI NL	SWR	04/2010	N.A.	377.93	986.3	608.37
159	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	SWR	04/2013	N.A.	558	692.43	134.43
160	SHIMOGA-HARIHAR NL	SWR	04/2011	N.A.	562.74	832.47	269.73
161	GADAG-WADI NL	SWR	04/2013	N.A.	1117	1922	805
162	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	2500	19565	17065
163	BHANUPALI-BILASPUR BERI NL	NR	04/2008	N.A.	1046.88	2966.99	1920.11
164	JIND-SONEPAT (NL), NR	NR	01/2004	03/2012	238.56	740	501.44
165	ROHTAK-MEHAM HANSI	NR	04/2012	N.A.	287	576.18	289.18
166	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	SWR	04/2007	03/2013	482	874.57	392.57
167	TUMKUR-CHITRADURGA-DAVENGERE NL	SWR	04/2011	N.A.	913	1801.01	888.01
168	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	N.A.	320.66	913.48	592.82
169	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	N.A.	446	685.17	239.17
170	JAYANAGAR-DARBHANGA-NARKATIA GANJ (GC), ECR	ECR	04/1997	03/2012	501.69	1043.56	541.87
171	KATIHAR - JOGBANI (GC)(NEFR)	NFR	09/2001	12/2010	492.98	1727.27	1234.29
172	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR	ECR	04/2002	03/2009	921	2363	1442
173	PATNA GANGA BRIDGE (NL), ECR	ECR	04/2001	10/2007	624.47	2921	2296.53
174	MAHARAJGANJ-MASRAKH (NL) - NER	NER	04/2003	N.A.	218.19	343	124.81
175	NANDYAL-YERRAGUNTALA(NL), SCR	SCR	03/1996	02/2009	155.74	883	727.26
176	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	N.A.	330	1047	717

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

ROAD TRANSPORT AND HIGHWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
177	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	196	331.23	135.23
178	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	155.04	280.13	125.09
179	AGRA-BYPASS(NS-1/UP-1), NH-2,3	NHAI	12/2003	09/2007	348.16	465.5	117.34
180	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	1108	2288	1180
181	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	199.81	385.13	185.32
SHIPPING AND PORTS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
182	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	03/2007	04/2009	245.67	373.22	127.55
183	CONST. AND DEV. OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL	MUMBAI PORT	11/2007	12/2010	1228	1460	232
184	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	150	600	450
STEEL							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
185	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	343	488.4	145.4
186	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	RINL	10/2005	10/2009	8692	12291	3599
URBAN DEVELOPMENT							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
187	BANGALORE METRO RAIL PROJECT	M RTP	05/2006	06/2011	6395	11609	5214

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	07/2015	1,3171.00	2,2462.00	9291	79
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	09/2016	3492.00	5677.00	2185	72

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
3	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	NLC	10/2004	06/2009	04/2015	2030.78	3477.21	1446.43	70
4	TUTICORIN THERMAL POWER PROJECT- 2X500 MW	NLC	05/2008	03/2012	04/2015	4904.54	6602.74	1698.2	37
5	ADRIYALA SHAFT PROJECT	SCCL	12/2009	03/2013	09/2015	212.34	1228.39	1016.05	30
6	MAGADH OC 20 MTY (CCL)	CCL	08/2008	07/2012	03/2016	469.78	706.40	236.62	44

PETROCHEMICALS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
7	ASSAM GAS CRACKER PROJECT	BCPL	04/2006	04/2012	06/2015	5460.61	9834.00	4373.39	38

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
8	DEV OF G1 AND GS-15 (ONGCL)	ONGC	04/2003	04/2006	06/2015	429.82	3955.21	3525.39	110
9	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	11/2016	666.00	838.00	172	12
10	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	02/2016	871.35	1200.00	328.65	11
11	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	10/2015	993.00	1693.00	700	45
12	INTEGRATED DEVELOPMENT OF BASSEIN FIELD	ONGC	12/2012	02/2016	04/2017	3513.07	4619.94	1106.87	14
13	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	ISPRL	01/2006	10/2011	10/2015	732.00	1227.00	495	48
14	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG	ISPRL	01/2006	10/2011	10/2015	672.00	1178.35	506.35	48

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)	
15	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	10/2016	309.81	462.79	152.98	24
16	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	05/2016	2059.63	2665.65	606.02	14
17	PARADIP REFINERY PROJECT	IOCL	02/2009	11/2012	03/2015	2,9777.00	3,4555.00	4778	28
18	DEVELOPMENT OF B-193 CLUSTER FIELDS	ONGC	06/2007	08/2010	05/2015	3248.78	6000.00	2751.22	57

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
19	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2018	3919.59	7531.72	3612.13	111
20	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	NHPC	09/2005	09/2009	06/2016	1061.38	1929.15	867.77	81
21	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	09/2008	03/2016	1779.29	2159.07	379.78	90
22	BARH STPP(3X660MW) NTPC	NTPC	02/2005	12/2009	03/2018	8692.97	1,5095.67	6402.7	99
23	KOLDAM HEP (NTPC)	NTPC	10/2002	04/2009	06/2015	4527.15	7220.00	2692.85	74
24	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A	PGCIL	09/2010	03/2013	06/2015	2074.86	2348.37	273.51	27
25	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	08/2015	421.01	994.85	573.84	25
26	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	03/2016	573.99	1487.49	913.5	31
27	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	07/2014	11/2018	2491.58	3745.08	1253.5	52
28	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	03/2017	4375.35	6749.18	2373.83	66
29	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	12/2015	477.69	721.81	244.12	63
30	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	11/2016	3642.04	5497.72	1855.68	10

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)	
31	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	05/2018	2978.48	3846.30	867.82	62
32	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	07/2010	05/2018	1657.00	2978.86	1321.86	94
33	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS	PGCIL	12/2011	08/2014	04/2015	901.77	1025.28	123.51	8
34	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	10/2016	368.72	1381.71	1012.99	123
35	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	05/2015	1746.65	2228.71	482.06	9
36	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH	PGCIL	09/2011	12/2013	04/2015	1366.34	1606.38	240.04	16
37	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C	PGCIL	03/2011	03/2014	06/2015	2569.25	3105.51	536.26	15
38	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	03/2017	2496.90	4676.34	2179.44	87

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
39	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	NCR	04/1986	03/1994	03/2015	158.77	608.02	449.25	252
40	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	03/2016	495.44	1781.98	1286.54	144
41	NANDYAL-YERRAGUNTALA(NL), SCR	SCR	03/1996	02/2009	03/2015	155.74	883.00	727.26	73
42	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	03/2015	393.46	1026.00	632.54	96
43	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	12/2009	06/2015	108.00	432.72	324.72	66
44	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	03/2018	733.00	2531.34	1798.34	111
45	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2019	727.56	6570.75	5843.19	96
46	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	12/2019	293.97	1428.00	1134.03	174

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)	
47	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	03/2016	171.10	272.39	101.29	48
48	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	03/2019	5300.00	6821.29	1521.29	60
49	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	03/2017	325.00	1564.54	1239.54	84
50	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	12/2015	687.20	800.00	112.8	69
51	ETAWAH-MAINPURI (NL),NCR	NCR	04/1997	12/2008	10/2015	120.00	245.39	125.39	82
52	PATNA GANGA BRIDGE (NL), ECR	ECR	04/2001	10/2007	12/2015	624.47	2921.00	2296.53	98
53	BANKURA - DAMODAR (GC) (SER)	SER	03/1998	03/2005	12/2019	111.90	2371.85	2259.95	177
54	KATI HAR - JOGBANI (GC)(NEFR)	NFR	09/2001	12/2010	03/2018	492.98	1727.27	1234.29	87
55	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	M RTP	04/2012	03/2016	03/2018	632.68	816.55	183.87	24
56	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	03/2007	03/2016	895.00	1242.25	347.25	108
57	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	03/2016	1676.31	5500.00	3823.69	84
58	KATAKHAL TO BHAIRABI	NFR	04/1998	12/2012	03/2016	227.90	331.40	103.5	39
59	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2020	850.00	2973.42	2123.42	60
60	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	SWR	04/2007	03/2013	09/2015	482.00	874.57	392.57	30
61	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	4190.00	2850.52	51
62	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2018	619.34	2820.25	2200.91	47
63	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2018	813.34	2876.00	2062.66	48

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)	
64	RANCHI-LOHARDAGA(GC),SER	SER	04/1997	06/2004	12/2015	194.07	335.00	140.93	138
65	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2017	1500.00	4996.19	3496.19	110
66	GONDIA- JABALPUR(GC), (SECR)	SECR	02/1997	03/1998	12/2019	386.30	1544.40	1158.1	261
67	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2018	2500.00	1,9565.00	17065	193

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
68	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	06/2015	199.81	385.13	185.32	74
69	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	11/2015	1108.00	2288.00	1180	48
70	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	06/2015	155.04	280.13	125.09	79
71	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	06/2015	196.00	331.23	135.23	71
72	AGRA-BYPASS(NS-1/UP-1), NH-2,3	NHAI	12/2003	09/2007	06/2015	348.16	465.50	117.34	93

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
73	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	RINL	10/2005	10/2009	05/2015	8692.00	1,2291.00	3599	67

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

List of ongoing projects having cost overrun w.r.t. to revised schedule

(March 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
1	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]	05/2010	335.61 -	388.53	05/2012 -	03/2015	15.77
	Total		335.61 -	388.53			
	<u>COAL</u>						
2	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,477.21	06/2009 -	04/2015	71.23
3	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37
4	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	479.63	03/2013 -	03/2017	0.02
5	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	03/2016 -	03/2016	31.87
	Total		3,130.68 -	4,861.83			
	<u>PETROCHEMICALS</u>						
6	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	9,834.00	04/2012 -	06/2015	80.09
	Total		5,460.61 -	9,834.00			
	<u>PETROLEUM</u>						
7	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]	06/2007	3,248.78 -	6,000.00	08/2010 03/2012	05/2015	84.68
8	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	03/2012	14,225.00 -	16,504.00	05/2016 -	05/2016	16.02
9	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	450.55	03/2017 -	03/2017	27.79
10	MARKETING TERMINAL AT PARADEEP - [N16000168]	07/2009	199.75 -	239.73	07/2013 -	-	20.02
11	KOTA JOBNER PIPELINE PROJECT - [N16000170]	04/2011	276.26 -	276.27	12/2015 -	03/2015	0.00
12	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]	10/2013	429.06 -	429.06	10/2014 -	10/2015	0.00
13	MARKETING TOP AT KORBA - [N16000186]	01/2011	141.86 -	232.00	09/2016 -	12/2015	63.54

(March 2015)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	Total		18,873.27 -	24,131.61			
	<u>POWER</u>						
14	PARBATI HEP (4X200 MW) (NHPC) II - [180100210	09/2002	3,919.59 -	7,531.72	09/2009 -	12/2018	92.16
15	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221	09/2003	6,285.33 -	15,300.00	09/2010 -	-	143.42
16	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243	09/2005	1,061.38 -	1,929.15	09/2009 -	06/2016	81.76
17	KISHANGANGA HEP (3X110 MW) - [N18000031	01/2009	3,642.04 -	5,497.72	01/2016 -	11/2016	50.95
18	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042	08/2008	2,491.58 -	3,745.08	07/2014 -	11/2018	50.31
19	TRIPURA GAS BASED POWER PROJECT - [N18000071	07/2009	421.01 -	994.85	07/2013 -	08/2015	136.30
	Total		17,820.93 -	34,998.52			
	<u>RAILWAYS</u>						
20	VIRAMGAM-BHILDI(WR),GC - [220100062	04/1990	155.66 -	548.01	- 03/2010	-	252.06
21	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	925.30	- -	02/2014	643.63
22	AMRAVATI-NARKHER NL(CR) - [220100118	06/1994	663.01 175.30	725.00	06/1999 -	07/2012	9.35
23	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60
24	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135	04/1983	36.80 274.41	1,336.57	- -	03/2019	3,531.98
25	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	968.60	12/2012 -	-	218.62
26	CALICUT-MANGALORE (DL) (SR) - [220100151	02/1996	240.00 -	579.37	- -	02/2012	141.40
27	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	1,781.98	03/2004 -	03/2016	259.68
28	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181	02/1997	514.68 -	2,820.00	- -	-	447.91
29	HASSAN-BANGALORE VIA SHRAVANA- BELGOLA(NL),SWR [220100183	02/1997	295.00 -	1,289.92	- -	-	337.26
30	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,544.40	03/1998 -	12/2019	299.79
31	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
32	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	800.00	- -	-	414.30

(March 2015)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
33	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	155.74 164.36	883.00	02/2009 -	03/2015	466.97
34	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	227.00 -	2,135.00	- -	-	840.53
35	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]	03/1997	677.97 1,062.36	1,651.54	- -	03/2015	143.60
36	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	06/2017	233.08
37	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	218.24 236.41	645.00	- -	03/2015	195.55
38	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	03/2015	160.76
39	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	194.07 -	335.00	06/2004 -	12/2015	72.62
40	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
41	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	1,630.97	05/2008 -	-	558.55
42	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	04/1997	501.69 335.77	1,043.56	03/2012 -	-	108.01
43	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	12/2009 -	06/2015	300.67
44	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	492.98 -	1,727.27	12/2010 -	03/2018	250.37
45	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00 -	1,566.00	- -	-	184.73
46	GULBARGA-BIDAR,SCR(NL) - [220100254]	02/1998	242.42 369.70	844.00	- 05/2009	03/2015	248.16
47	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR- NAUTANWA GC (NER) [220100255]	04/1997	863.23 -	1,072.51	- -	06/2015	24.24
48	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	625.30 408.76	847.75	06/2007 -	-	35.57
49	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	100.00 -	980.00	- -	-	880.00
50	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) [220100263]	03/1998	280.00 -	1,122.00	- -	-	300.71
51	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 -	1,047.00	- -	-	217.27
52	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	2,531.34	12/2008 -	03/2018	245.34
53	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM- NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
54	GADWAL - RAICHUR (NL), SCR - [220100270]	04/1998	92.63 -	270.00	02/2011 -	-	191.48

(March 2015)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
55	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	04/1996	138.00 -	1,382.78	- -	-	902.01
56	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	2,371.85	03/2005 12/2008	12/2019	2,019.62
57	JIND-SONEPAT (NL),NR - [220100280	01/2004	238.56 -	740.00	03/2012 -	12/2012	210.19
58	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	470.21 -	1,995.25	- -	-	324.33
59	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06
60	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	288.00	02/2009 02/2009	08/2014	73.33
61	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	6,570.75	03/2011 -	03/2019	803.12
62	KOSI BRIDGE (NL), ECR - [220100304	04/2002	322.95 -	341.41	03/2012 -	-	5.72
63	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	03/2009 -	12/2014	156.57
64	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76
65	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314	04/2001	470.92 727.13	1,225.90	- -	03/2017	160.32
66	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315	01/2004	915.70 -	3,700.00	- -	03/2015	304.06
67	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316	04/2003	218.19 -	343.00	- -	-	57.20
68	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	1,101.16	- -	03/2017	186.92
69	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	818.29	02/2015 -	02/2015	346.59
70	CUTTACK - BARANG (LD) - [220100326	04/1995	127.13 -	225.00	- -	10/2014	76.98
71	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	276.00	03/2009 03/2009	08/2014	106.88
72	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	810.78 -	810.80	- -	-	0.00
73	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329	04/2003	136.62 -	289.93	12/2007 03/2010	-	112.22
74	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	332.92 283.95	477.88	03/2012 -	-	43.54
75	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N220000032	04/2006	378.56 -	791.59	- -	-	109.11
76	GOELKERA-MANOHARPUR,(LD)(SER) - [N220000045	03/1997	261.70 -	280.00	02/2006 -	-	6.99
77	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N220000049	07/2006	743.00 -	1,117.11	03/2008 06/2008	-	50.35
78	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N220000075	09/2006	324.90 -	385.54	03/2010 -	-	18.66

(March 2015)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
79	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41
80	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' - AGASTIYAMPALLI - [N22000079]	09/2007	404.19 -	1,383.45	- -	-	242.28
81	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	914.98	- -	03/2015	166.63
82	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	485.00	03/2011 -	-	185.29
83	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 -	490.00	- -	-	292.00
84	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	1,080.00	- -	-	136.84
85	NEW B.G. LINE FROM TETELIA TO BYRNHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	496.24	- -	03/2017	148.12
86	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	300.00 -	827.73	- -	03/2019	175.91
87	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,564.54	03/2010 -	03/2017	381.40
88	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	6,821.29	03/2014 -	03/2019	28.70
89	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	272.39	03/2012 -	03/2016	59.20
90	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,428.00	06/2005 -	12/2019	385.76
91	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	2,876.00	03/2014 -	03/2018	253.60
92	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,820.25	04/2014 -	03/2018	355.36
93	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	565.13	- -	03/2018	99.75
94	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,190.00	12/2015 -	03/2020	212.81
95	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]	04/2007	482.00 -	874.57	03/2013 -	09/2015	81.45
96	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	653.55	03/2014 -	-	0.06
97	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012 -	-	135.68
98	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	-	1.06
99	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	850.00 -	2,973.42	03/2015 -	03/2020	249.81
100	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41

(March 2015)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
101	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	5,500.00	03/2009 -	03/2016	228.10
102	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	494.92	- -	-	67.77
103	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	685.17	- -	-	53.63
104	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	3,500.00	- -	-	68.05
105	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	262.00	- -	-	10.58
106	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR - [N22000152]	04/2013	456.00 -	855.16	- -	-	87.54
107	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	-	17.92
108	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	218.39	- -	-	2.34
109	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00	- -	-	62.32
110	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00	- -	12/2019	82.25
111	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
112	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44
113	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	03/2016	88.40
114	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	12/2017	41.36
115	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
116	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
117	HAJIPUR-RAMDALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
118	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00 -	1,887.90	- -	03/2019	5.00
119	ATTIPPATTU-PUTTUR - [N22000184]	04/2008	446.87 -	528.00	- -	-	18.16
120	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,200.00	- -	-	129.22
121	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
122	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17

(March 2015)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
123	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]	04/1998	271.24 -	520.00	- -	-	91.71
124	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,280.83	- -	-	55.74
125	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
126	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	563.13	- -	03/2019	154.33
127	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,242.25	03/2007 -	03/2016	38.80
128	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00 -	886.65	- -	03/2018	251.85
129	DIMAPUR-TIZIT NL - [N22000196]	04/2013	4,274.00 -	4,487.70	- -	-	5.00
130	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77 -	441.45	- -	03/2018	110.44
131	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	288.81	- -	03/2018	1.86
132	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22	- -	-	109.04
133	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	-	173.71
134	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	247.00 -	951.24	- -	03/2015	285.12
135	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	222.95	- -	-	16.29
136	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02 -	5,307.90	- -	03/2020	30.00
137	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	679.57	- -	03/2018	180.56
138	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	03/2017	63.25
139	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	435.58	- -	03/2018	162.68
140	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]	04/1999	523.17 -	1,653.55	- -	03/2018	216.06
141	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12 -	453.10	- -	03/2018	45.17
142	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	364.06	- -	03/2019	47.95
143	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	03/2018	29.06
144	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	800.00	- -	-	33.02
145	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	499.30 -	2,501.05	- -	-	400.91

(March 2015)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
146	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70 -	279.70	- -	-	0.72
147	PEN ROHA DOUBLING - [N22000254]	04/2007	98.74 -	203.00	- -	03/2015	105.59
148	PANVEL PEN DOUBLING - [N22000255]	04/2006	96.16 -	260.16	- -	01/2015	170.55
149	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26
150	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	-	651.97
151	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97
152	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]	04/2008	184.26 -	2,000.00	- -	-	985.42
153	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	576.18	- -	-	100.76
154	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99	- -	-	183.41
155	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	-	24.09
156	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	-	57.65
157	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	- -	-	47.93
158	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,743.00	- -	-	79.63
159	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29
160	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	329.97	- -	-	50.10
161	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	-	14.14
162	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00	- -	-	72.07
163	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	-	12.38
164	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]	04/1999	460.94 -	1,030.00	01/1999 -	-	123.46
165	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	800.00	01/1999 -	-	71.50
166	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	01/1999 -	-	53.96
167	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	679.27 -	1,111.99	- -	-	63.70
168	JHARSUGUDA-RENGALI DOUBLING - [N22000317]	03/2006	201.00 -	230.00	- -	-	14.43
169	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	826.57 -	1,143.60	- -	03/2018	38.35

(March 2015)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
170	DELANG-PURI DOUBLING - [N22000320]	03/2011	165.16 -	234.71	03/2015 -	03/2015	42.11
171	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10
172	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	209.00	12/2016 -	12/2016	40.49
	Total		80,238.02 -	202128.68			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
173	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00 -	201.66	09/2008 -	03/2015	30.10
174	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	12/2015	28.93
175	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	06/2015	92.75
176	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	06/2015	80.68
177	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	06/2015	68.99
178	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	02/2017	2.29
179	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]	12/2003	348.16 -	465.50	09/2007 -	06/2015	33.70
180	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	11/2015	106.50
	Total		2,717.01 -	4593.96			
	<u>SHIPPING AND PORTS</u>						
181	CONST. AND DEV. OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016]	11/2007	1,228.00 -	1,460.00	12/2010 -	-	18.89
182	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	03/2006 -	-	300.00
183	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]	03/2007	245.67 -	373.22	04/2009 -	-	51.92
	Total		1,623.67 -	2,433.22			
	<u>STEEL</u>						
184	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	10/2016 -	10/2016	42.39
	Total		343.00 -	488.40			
	<u>URBAN DEVELOPMENT</u>						

(March 2015)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
185	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00 -	11,609.00	06/2011 -	-	81.53
	Total		6,395.00 -	11,609.00			
	Grand Total		136,937.80	2,95,467.75			

List of Projects Ahead of Schedule w.r.t. Latest Schedule

(March 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>PETROLEUM</u>						
1	DEV OF G1 AND GS-15 (ONGCL) - [160100231	4/2003	429.82 3,955.21	3,955.21	3,439.48	04/2006 04/2016	06/2015
2	KOTA JOBNER PIPELINE PROJECT - [N16000170	4/2011	276.26 -	276.27	241.63	12/2015 -	03/2015
3	MARKETING TOP AT KORBA - [N16000186	1/2011	141.86 -	232.00	126.07	09/2016 -	12/2015
	Total		847.94 -	4,463.48	3,807.18		
	<u>POWER</u>						
4	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) [N18000154	10/2013	1,315.90 -	1,315.90	365.47	10/2016 -	03/2016
	Total		1,315.90 -	1,315.90	365.47		
	Grand Total		2,163.84	5,779.38	4,172.65		

List of Projects on schedule w.r.t. Latest Schedule

(March 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	9/2003	3,492.00 -	5,677.00	4,933.80	09/2010 09/2016	09/2016
	Total		3,492.00 -	5,677.00	4,933.80		
	<u>COAL</u>						
2	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	1,188.31	756.61	03/2023 03/2023	03/2023
3	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]	12/2009	1,352.04 -	1,143.54	778.29	03/2016 -	03/2016
4	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	0.46	03/2023 03/2023	03/2023
5	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	98.00	03/2020 -	03/2020
6	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	94.90	03/2016 -	03/2016
7	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) [N06000091]	6/2011	1,131.28 -	1,131.28	77.88	03/2018 -	03/2018
8	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	6/2011	5,907.11 -	5,907.11	784.75	12/2015 04/2018	04/2018
9	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]	4/2012	258.56 -	258.56	74.44	03/2016 -	03/2016
10	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	0.65	03/2026 -	03/2026
11	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]	5/2014	479.15 -	479.15	6.34	03/2019 -	03/2019
12	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	22.10	03/2020 -	03/2020
13	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]	8/2012	1,055.05 -	1,055.05	148.67	03/2018 -	03/2018
14	KAPURIA UG(PSLW) - [N06000108]	8/2011	988.35 -	988.35	6.84	04/2017 -	04/2017
15	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	6.84	03/2021 -	03/2021
16	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.33	-	03/2022 -	03/2022
17	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	101.90	03/2020 -	03/2020
18	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	430.14	69.91	03/2016 -	03/2016

(March 2015)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
19	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	30.24	03/2021 -	03/2021
20	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	106.44	03/2021 -	03/2021
21	AMERA OC RCE - [N06000123]	2/2015	335.97 -	335.97	30.30	03/2018 -	03/2018
22	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
23	BHANEGAON OC - [N06000121]	2/2015	187.94 -	187.94	20.59	03/2023 -	03/2023
24	GOKUL - [N06000120]	11/2014	267.67 -	267.67	68.35	03/2018 -	03/2018
25	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	61.70	03/2021 -	03/2021
26	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	6.02	03/2020 -	03/2020
27	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	2.49	03/2021 -	03/2021
28	KULDA EXPN OC. (5.00 MTY) - [N06000115]	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
29	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]	5/2014	337.66 -	337.66	-	03/2019 -	03/2019
30	MOONIDIH XV SEAM UG - [N06000098]	8/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015
31	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	7/2011	162.76 -	162.76	2.48	03/2015 -	03/2015
32	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]	12/2009	510.85 -	510.85	223.68	03/2016 -	03/2016
33	RKP OCP PHASE-I - [N06000079]	3/2010	209.78 -	209.78	74.96	03/2015 -	03/2015
34	BATURA OCP (2.0 MTY) - [N06000049]	9/2008	203.82 -	203.82	-	03/2015 -	03/2015
35	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.10 -	490.10	186.68	03/2017 -	03/2017
	Total		35,065.49 -	28,480.36	3,842.51		
	<u>FERTILISERS</u>						
36	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	197.79	12.09	11/2016 -	11/2016
	Total		197.79 -	197.79	12.09		
	<u>MINES</u>						
37	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]	9/2011	1,856.00 -	1,856.00	-	09/2017 -	09/2017

(March 2015)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		1,856.00 -	1,856.00	.00		
	<u>PETROLEUM</u>						
38	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]	6/2007	736.65 -	736.65	472.24	09/2011 12/2015	12/2015
39	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]	7/2008	288.04 288.04	253.66	218.56	08/2012 03/2015	03/2015
40	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]	6/2010	2,523.00 -	2,523.00	1,019.79	01/2014 12/2015	12/2015
41	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]	11/2010	331.20 -	269.10	190.04	08/2013 05/2015	05/2015
42	MEHESANA REDEVELOPMENT PROJECT - [N16000121]	11/2010	3,823.00 -	3,823.00	1,076.57	04/2015 12/2017	12/2017
43	102 MW WIND POWER PROJECT - [N16000119]	7/2010	1,106.00 -	678.02	405.00	06/2012 03/2015	03/2015
44	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]	1/2010	723.64 -	723.64	-	03/2013 06/2016	06/2016
45	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]	6/2010	202.94 -	188.89	2.00	01/2014 11/2017	11/2017
46	TWENTY NOS. FEEDER GAS LINES - [N16000192]	3/2009	228.64 -	214.19	122.59	12/2016 -	12/2016
47	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]	12/2011	160.00 -	160.00	2.32	02/2016 -	02/2016
48	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]	7/2014	419.04 -	419.04	27.85	01/2017 -	01/2017
49	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	6/2014	5,706.47 -	5,813.25	300.65	05/2017 05/2017	05/2017
50	RESID UPGRADATION PROJECT - [N16000184]	2/2011	3,110.36 -	3,110.36	508.71	11/2015 -	11/2015
51	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]	3/2014	2,476.82 -	2,476.82	-	12/2018 -	12/2018
52	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]	10/2013	429.06 -	429.06	-	10/2014 10/2015	10/2015
53	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS - [N16000181]	3/2013	2,913.10 -	2,913.10	9.72	05/2016 04/2018	04/2018
54	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]	2/2014	163.88 -	163.88	14.86	07/2016 -	07/2016
55	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00 -	3,150.00	96.36	09/2017 -	09/2017
56	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]	4/2013	480.00 -	480.00	23.70	02/2016 -	02/2016

(March 2015)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
57	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]	3/2014	3,076.00 -	3,076.00	91.65	09/2017 -	09/2017
58	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	5/2013	4,124.35 -	4,124.35	75.24	04/2016 04/2016	04/2016
59	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	2/2012	666.00 -	838.00	443.65	11/2015 11/2016	11/2016
60	REWARI KANPUR PIPELINE PROJECT - [N16000145]	2/2012	1,210.64 -	1,446.34	982.15	11/2015 -	11/2015
61	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	3/2012	14,225.00 -	16,504.00	5,828.23	05/2016 -	05/2016
62	IOR OF B-173A FIELD - [N16000140]	1/2012	352.49 -	352.49	104.58	03/2014 04/2015	04/2015
63	PIPELINE REPLACEMENT PROJECT-3 - [N16000137]	4/2012	2,547.26 -	1,417.00	1,410.50	05/2014 05/2015	05/2015
64	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]	4/2012	600.17 -	600.17	249.17	12/2014 05/2015	05/2015
65	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]	3/2012	2,592.17 -	2,592.17	534.59	05/2014 03/2016	03/2016
66	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]	3/2012	5,608.40 -	5,608.40	3,576.16	05/2015 -	05/2015
67	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	854.43	03/2015 05/2016	05/2016
68	LPG TERMINAL AT KOCHI - [N16000171]	12/2012	607.06 -	607.06	57.79	01/2016 04/2017	04/2017
69	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	7/2011	352.56 -	450.55	10.60	03/2017 -	03/2017
70	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]	4/2010	270.00 -	215.66	-	06/2012 11/2015	11/2015
71	SURAT PARADIP PIPELINE PROJECT - [N16000163]	10/2012	10,281.00 -	10,281.00	1.36	04/2015 -	04/2015
72	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]	3/2013	1,138.50 -	686.58	-	04/2015 04/2015	04/2015
73	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]	12/2012	3,513.07 -	4,619.94	0.47	02/2016 04/2017	04/2017
74	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]	9/2011	202.25 -	160.16	39.42	07/2016 -	07/2016
75	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79	215.01	10/2014 10/2016	10/2016
76	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]	2/2011	913.00 -	913.00	379.89	08/2015 -	08/2015
	Total		83,621.20 -	86,146.97	19,345.85		
	<u>POWER</u>						
77	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	4,676.34	3,824.04	12/2009 03/2017	03/2017

(March 2015)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
78	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	8/2008	2,491.58 -	3,745.08	592.40	07/2014 11/2018	11/2018
79	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]	9/2011	1,366.34 -	1,606.38	1,268.66	12/2013 04/2015	04/2015
80	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	346.79	262.57	08/2014 06/2015	06/2015
81	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]	3/2011	2,569.25 -	3,105.51	2,729.47	03/2014 06/2015	06/2015
82	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]	9/2010	2,074.86 -	2,348.37	1,764.24	03/2013 06/2015	06/2015
83	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]	12/2011	901.77 -	1,025.28	867.80	08/2014 04/2015	04/2015
84	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	11,846.00	3,718.00	06/2017 -	06/2017
85	TRANS. SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]	6/2014	400.47 -	400.47	-	04/2017 -	04/2017
86	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]	2/2014	378.71 -	378.71	34.00	10/2016 -	10/2016
87	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 -	522.29	-	11/2016 -	11/2016
88	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]	5/2014	303.07 -	303.07	1.00	07/2016 -	07/2016
89	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]	5/2014	829.98 -	829.98	-	08/2016 -	08/2016
90	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]	2/2014	167.40 -	167.40	3.00	12/2015 -	12/2015
91	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]	2/2014	243.53 -	243.53	44.00	08/2016 -	08/2016
92	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	2/2014	908.08 -	908.08	20.00	06/2016 -	06/2016
93	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]	2/2014	539.82 -	539.82	14.00	06/2016 -	06/2016
94	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58 -	14,366.58	2,056.00	02/2019 -	02/2019
95	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	12,532.44	1,408.00	08/2018 -	08/2018
96	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	578.00	03/2019 -	03/2019
97	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]	11/2014	972.42 -	972.42	-	11/2017 -	11/2017
98	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]	10/2014	8,112.12 -	8,112.12	-	04/2020 -	04/2020

(March 2015)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
99	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	2/2014	196.58 -	196.58	-	02/2016 -	02/2016
100	TRANS. SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. [N18000170]	8/2014	188.75 -	188.75	-	02/2017 -	02/2017
101	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID [N18000169]	8/2014	288.49 -	288.49	-	02/2017 -	02/2017
102	TRANS.SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	442.00	03/2018 -	03/2018
103	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION [N18000186]	3/2015	550.06 -	550.06	-	04/2018 -	04/2018
104	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]	3/2015	1,071.24 -	1,071.24	-	10/2017 -	10/2017
105	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]	3/2015	197.40 -	197.40	-	04/2018 -	04/2018
106	WARDHA-HYDERABAD 765 KV LINK - [N18000183]	1/2015	3,662.02 -	3,662.02	-	05/2018 -	05/2018
107	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	1/2015	203.28 -	203.28	-	07/2017 -	07/2017
108	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) [N18000181]	1/2015	871.62 -	871.62	-	10/2017 -	10/2017
109	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP [N18000180]	1/2015	268.80 -	268.80	-	03/2018 -	03/2018
110	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) [N18000179]	12/2014	6,517.36 -	6,517.36	-	04/2018 -	04/2018
111	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.84	109.00	09/2019 -	09/2019
112	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]	3/2015	1,394.52 -	1,394.52	-	06/2017 -	06/2017
113	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]	1/2014	374.63 -	374.63	-	04/2016 -	04/2016
114	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,364.52	135.34	04/2016 -	04/2016
115	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]	9/2013	1,575.30 -	1,575.30	214.60	05/2016 -	05/2016
116	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV [N18000152]	9/2013	680.69 -	680.69	164.49	03/2016 -	03/2016
117	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	11,638.55	2,772.00	09/2017 -	09/2017
118	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]	3/2013	2,514.88 -	2,514.88	480.65	12/2015 -	12/2015

(March 2015)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
119	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	3/2013	514.20 -	514.20	102.00	06/2015 -	06/2015
120	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	147.00	08/2017 -	08/2017
121	VINDHYACHAL STPP STAGE-V - [N18000134]	5/2012	3,180.40 -	3,180.40	1,740.00	08/2015 -	08/2015
	Total		118,823.42 -	123,479.14	25,492.26		
	<u>RAILWAYS</u>						
122	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	4/2006	325.00 -	1,564.54	420.71	03/2010 03/2017	03/2017
123	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	4/2010	2,913.51 -	2,619.02	525.84	03/2016 -	03/2016
124	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]	4/2008	829.74 -	829.74	93.08	03/2015 -	03/2015
125	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	4/2010	3,951.98 -	3,951.98	584.90	03/2016 -	03/2016
126	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	4/2008	5,300.00 -	6,821.29	2,217.14	03/2014 03/2019	03/2019
127	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	4/2006	850.00 -	2,973.42	10.44	03/2015 03/2020	03/2020
128	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	1,176.09 -	3,845.60	2.33	02/2020 -	02/2020
129	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	4/2012	148.77 -	209.00	2.64	12/2016 -	12/2016
130	DELANG-PURI DOUBLING - [N22000320]	3/2011	165.16 -	234.71	137.01	03/2015 -	03/2015
131	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	4/2010	423.66 -	423.66	263.01	03/2017 -	03/2017
132	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	4/2011	299.60 -	299.60	1.10	03/2017 -	03/2017
133	PLASSEY-JIAGANJ DOUBLING - [N22000220]	4/2011	248.07 -	248.07	29.10	03/2015 -	03/2015
134	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]	4/2010	622.41 -	2,030.50	3.61	02/2019 -	02/2019
135	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	3/2013	4,874.58 -	4,874.58	2,371.00	03/2016 -	03/2016
	Total		22,128.57 -	30,925.71	6,661.91		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						

(March 2015)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
136	GUWHATI TO NALBARI (AS-4) - [N24000038]	12/2003	175.96 -	175.96	290.20	04/2008 04/2015	04/2015
137	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 [N24000233]	4/2014	1,266.60 -	1,266.60	-	09/2016 -	09/2016
138	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) [N24000232]	11/2013	1,916.79 -	1,916.79	-	11/2016 -	11/2016
139	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]	10/2013	283.25 -	283.25	-	10/2015 -	10/2015
140	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	-	12/2015 -	12/2015
141	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	-	09/2015 -	09/2015
142	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	457.70	04/2010 01/2016	01/2016
143	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]	12/2003	160.00 -	160.00	211.80	05/2008 06/2015	06/2015
144	NALBARI TO BIJNI (AS-6) - [N24000047]	12/2003	225.00 -	225.00	276.70	06/2008 04/2015	04/2015
145	SONAPUR TO GUWAHTI (AS-3) - [N24000044]	12/2003	245.00 -	245.00	491.20	03/2008 03/2015	03/2015
	Total		8,188.45 -	8,280.40	1,727.60		
	<u>STEEL</u>						
146	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]	11/2012	313.05 -	313.05	205.93	06/2015 -	06/2015
147	REBUILDING OF COB-7 AT BSL - [N12000083]	10/2013	245.67 -	245.67	32.31	05/2016 -	05/2016
148	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]	6/2014	708.91 -	708.91	99.30	04/2016 -	04/2016
149	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]	4/2014	188.93 -	188.93	16.95	04/2015 -	04/2015
150	NMDC INTEGRATED STEEL PLANT - [N12000086]	1/2010	15,525.00 -	15,525.00	6,655.07	05/2015 12/2016	12/2016
151	3RD CONVERTER AND 4TH CASTER - [N12000088]	7/2011	974.76 -	974.76	69.15	07/2016 -	07/2016
152	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	23.52	10/2016 -	10/2016
153	TURBO BLOWER - 5 - [N12000092]	12/2009	280.00 -	280.00	2.00	09/2016 -	09/2016
154	ALTERNATE GAS NETWORK AT BSL - [N12000093]	3/2015	255.19 -	255.19	-	03/2018 -	03/2018
	Total		18,834.51 -	18,979.91	7,104.23		

(March 2015)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>TELECOMMUNICATIONS</u>						
155	NETWORK FOR SPECTRUM - [N26000101]	3/2012	13,334.00 -	13,334.00	360.00	07/2015 -	07/2015
	Total		13,334.00 -	13,334.00	360.00		
	<u>URBAN DEVELOPMENT</u>						
156	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]	2/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019
157	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,219.21	-	07/2017 -	07/2017
158	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]	6/2014	157.84 -	157.84	2.31	03/2017 -	03/2017
159	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,264.00	421.28	11/2019 -	11/2019
160	KOCHI METRO RAIL PROJECT - [N28000081]	7/2012	5,181.79 -	5,181.79	806.39	07/2017 -	07/2017
161	NAGPUR METRO RAIL - [N28000085]	8/2014	8,680.00 -	8,680.00	-	03/2018 -	03/2018
	Total		45,907.98 -	45,907.98	1,229.98		
	Grand Total		351,449.41	363,265.26	70,710.23		

List of Delayed Projects w.r.t. Latest Schedule

(March 2015)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00 22,462.00	22,462.00	18,271.00	12/2008 10/2013	07/2015	79	21
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	6,297.00	12/2015 -	10/2017	22	-
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	4,053.00	12/2016 -	05/2018	17	-
	Total		36,950.00 -	46,241.00	28,621.00				
	<u>CIVIL AVIATION</u>								
4	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 -	388.53	295.43	05/2012 -	03/2015	34	-
5	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]AAI,CHANDIGARH	02/2011	452.00 489.00	452.00	410.25	03/2015 -	04/2015	1	-
6	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	344.28	52.48	03/2014 -	04/2015	13	-
7	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	217.60	0.04	03/2015 -	09/2015	6	-
8	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	309.46	338.57	01/2011 -	06/2016	65	-
	Total		1,658.95 -	1,711.87	1,096.77				
	<u>COAL</u>								
9	PURNADIIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	186.69	03/2013 -	03/2015	24	-
10	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,TAMIL NADU	10/2004	2,030.78 3,027.59	3,477.21	3,185.95	06/2009 03/2013	04/2015	70	25
11	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	6,115.69	03/2012 05/2014	04/2015	37	11
12	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]NLC,TAMIL NADU	04/2012	364.75 -	364.75	128.27	10/2014 -	06/2015	8	-
13	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,TELANGANA	12/2009	212.34 1,228.39	1,228.39	879.85	03/2013 09/2012	09/2015	30	36
14	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,648.31	03/2014 -	03/2016	24	-
15	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,607.84	03/2014 -	03/2016	24	-
16	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,UTTAR PRADESH	06/2011	789.88 -	741.62	464.94	03/2013 -	03/2016	36	-
17	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,MADHYA PRADESH	06/2011	746.04 -	535.10	348.33	03/2015 -	03/2016	12	-

(March 2015)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
18	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	469.78 -	706.40	53.38	07/2012 -	03/2016	44	-
19	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 -	259.40	12.52	03/2012 -	03/2016	48	-
20	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35 -	462.35	273.72	03/2014 -	03/2016	24	-
21	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	55.48	03/2014 -	03/2016	24	-
22	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24	-
23	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	418.97	326.51	03/2012 -	03/2016	48	-
24	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	181.19	36.60	03/2012 -	03/2016	48	-
25	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	211.71	03/2014 -	03/2016	24	-
26	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	35.68	03/2011 -	03/2016	60	-
27	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	149.41	03/2012 -	03/2016	48	-
28	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	6.56	06/2015 -	03/2016	9	-
29	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	132.68	03/2010 -	03/2017	84	-
30	ASHOK EXPN OCP CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	471.66 341.63	341.63	117.84	03/2011 -	03/2017	72	-
31	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL	11/2006	287.18 -	287.17	142.59	03/2011 -	03/2017	72	-
32	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	162.21	03/2013 -	03/2017	48	-
33	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	148.02	03/2010 -	03/2017	84	-
34	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	453.63	104.49	12/2012 -	03/2017	51	-
35	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	172.80	03/2012 -	03/2017	60	-
36	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	479.63	118.94	03/2013 -	03/2017	48	-
37	JAGANNATHPOR OC - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	152.43	21.55	03/2015 -	03/2017	24	-
38	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	75.71	03/2012 -	03/2017	60	-
39	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	69.64	03/2014 -	03/2017	36	-
40	KALYANIKHANI OPENCASE PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	417.33	11.41	07/2016 -	03/2017	8	-
41	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	242.29	0.03	03/2015 -	03/2018	36	-
42	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	447.06	29.03	03/2015 -	03/2018	36	-
43	TALABIRA OCP - [N06000043]MCL,ODISHA	03/2008	447.72 -	447.72	52.36	03/2016 -	03/2020	48	-

(March 2015)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
44	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL, ODISHA	02/2008	395.87 -	395.87	76.74	03/2015 -	03/2021	72	-
	Total		22,394.41 -	26,402.57	17,163.48				
	<u>STEEL</u>								
45	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]NMDC, CHHATISGARH	01/2007	607.17 -	607.17	386.96	12/2011 01/2015	03/2015	39	2
46	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL, ANDHRA PRADESH	10/2005	8,692.00 12,291.00	12,291.00	11,284.83	10/2009 10/2012	05/2015	67	31
47	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL, JHARKHAND	05/2010	6,325.00 -	6,325.00	5,097.28	12/2011 -	05/2015	41	-
48	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL, WEST BENGAL	08/2010	2,875.00 -	2,875.00	2,567.13	12/2012 -	05/2015	29	-
49	CAPTIVE POWER PLANT - 2 - [N12000087]RINL, ANDHRA PRADESH	02/2011	677.00 -	677.00	509.41	09/2013 -	05/2015	20	-
50	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]RINL, MULTI STATE	07/2007	480.00 -	450.00	375.17	09/2009 05/2012	06/2015	69	37
51	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC, KARNATAKA	04/2011	572.00 -	572.00	451.58	04/2013 09/2014	06/2015	26	9
52	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL, ODISHA	11/2011	254.55 -	254.55	123.28	11/2013 -	06/2015	19	-
53	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHHATISGARH - [N12000078]SAIL, CHHATISGARH	07/2012	332.65 -	332.65	172.77	08/2014 -	06/2015	10	-
54	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL, ODISHA	10/2012	160.48 -	160.48	118.88	09/2014 -	06/2015	9	-
55	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC, KARNATAKA	02/2011	898.55 -	898.55	379.57	05/2013 01/2015	08/2015	27	7
56	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL, MAHARASHTRA	12/2011	187.33 -	187.33	149.44	10/2013 -	08/2015	22	-
57	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODISHA - [N12000079]SAIL, ODISHA	06/2012	237.09 -	237.09	155.48	12/2014 -	08/2015	8	-
58	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, CHHATISGARH	08/2010	17,265.00 -	17,265.00	14,300.13	03/2013 -	09/2015	30	-
59	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL, ANDHRA PRADESH	07/2011	877.73 -	877.73	164.04	07/2015 -	03/2016	8	-
60	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL, ANDHRA PRADESH	05/2012	404.16 -	404.16	144.33	07/2015 -	03/2017	20	-
	Total		40,845.71 -	44,414.71	36,380.28				
	<u>PETROCHEMICALS</u>								
61	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, ASSAM	04/2006	5,460.61 8,920.00	9,834.00	8,459.13	04/2012 12/2013	06/2015	38	18
	Total		5,460.61 -	9,834.00	8,459.13				

(March 2015)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	PETROLEUM								
62	PARADIP REFINERY PROJECT - [N16000058]IOCL,ODISHA	02/2009	29,777.00 34,555.00	34,555.00	28,733.70	11/2012 11/2013	03/2015	28	16
63	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 761.68	761.68	728.35	05/2013 06/2014	03/2015	22	9
64	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL,MAHARASHTRA	03/2012	1,419.00 -	1,419.00	1,108.86	12/2014 -	03/2015	3	-
65	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,MAHARASHTRA	06/2007	3,248.78 5,633.44	6,000.00	5,925.40	08/2010 03/2012	05/2015	57	38
66	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00 -	2,915.00	1,339.14	12/2012 -	06/2015	30	-
67	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	429.00	278.78	06/2011 03/2012	07/2015	49	40
68	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL,TAMIL NADU	12/2012	279.00 -	279.00	142.28	12/2014 06/2015	07/2015	7	1
69	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	317.64 -	240.95	111.38	09/2012 04/2015	10/2015	37	6
70	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,ANDHRA PRADESH	01/2006	672.00 1,178.35	1,178.35	1,099.88	10/2011 -	10/2015	48	-
71	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	944.84	10/2011 -	10/2015	48	-
72	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,398.50	01/2012 -	10/2015	45	-
73	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA	12/2009	1,584.00 -	1,584.00	1,193.37	08/2015 -	12/2015	4	-
74	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,MULTI STATE	08/2011	586.00 -	586.00	295.67	08/2015 -	12/2015	4	-
75	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96 -	191.96	77.79	05/2015 -	12/2015	7	-
76	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 1,200.00	1,200.00	180.26	03/2015 11/2015	02/2016	11	3
77	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 -	2,378.89	1,768.09	03/2013 03/2015	03/2016	36	12
78	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	1,087.70	09/2012 -	03/2016	42	-
79	IMPROVED OIL RECOVERY OF B-173A FIELD - [N16000185]ONGC,MAHARASHTRA	01/2012	352.49 -	352.49	104.58	03/2014 -	03/2016	24	-
80	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC,MULTI STATE	04/2013	284.82 -	284.82	-	04/2015 04/2015	05/2017	25	25
81	AHMEDABAD REDEVELOPMENT PROJECT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10 -	1,916.10	1,161.74	12/2014 -	12/2017	36	-
82	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63 -	2,189.63	1,035.48	12/2014 -	12/2018	48	-

(March 2015)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
83	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18 -	7,596.18	17.06	01/2013 -	02/2019	73	-
	Total		61,509.21 -	70,771.05	48,732.85				
	<u>POWER</u>								
84	BARH STPP STAGE -II - [N18000047]NTPC,BIHAR	02/2008	7,341.04 -	7,341.04	8,594.00	10/2013 -	03/2015	17	-
85	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATISGARH	05/2011	1,961.87 -	1,961.87	1,653.45	05/2014 -	03/2015	10	-
86	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL,MADHYA PRADESH	03/2012	213.78 -	213.78	190.44	03/2014 -	03/2015	12	-
87	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL,MULTI STATE	02/2012	1,927.16 -	1,927.16	1,462.27	10/2014 -	04/2015	6	-
88	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH	11/2011	2,127.51 -	2,127.51	2,129.33	07/2014 -	05/2015	10	-
89	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 2,228.71	2,228.71	863.63	08/2014 -	05/2015	9	-
90	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	171.92	04/2015 -	05/2015	1	-
91	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]PGCIL,MULTI STATE	09/2012	803.34 -	803.34	544.89	03/2015 -	05/2015	2	-
92	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]NEEPCO,TRIPURA	07/2012	296.87 363.73	363.73	309.52	12/2014 -	05/2015	5	-
93	KOLDAM HEP (NTPC) - [180100211]NTPC,HIMACHAL PRADESH	10/2002	4,527.15 7,220.00	7,220.00	6,544.00	04/2009 -	06/2015	74	-
94	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	105.10	01/2013 -	06/2015	29	-
95	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,407.46	11/2013 -	06/2015	19	-
96	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,732.36	09/2014 -	06/2015	9	-
97	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	1,801.76	08/2014 -	06/2015	10	-
98	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	2,195.41	10/2014 -	06/2015	8	-

(March 2015)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
99	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,MULTI STATE	06/2012	1,263.26 -	1,263.26	1,006.48	11/2014 -	06/2015	7	-
100	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. - [N18000076]PGCIL,MULTI STATE	03/2010	4,672.99 -	4,672.99	3,607.97	11/2012 -	07/2015	32	-
101	TRIPURA GAS BASED POWER PROJECT - [N18000071]NNEEPCO,TRIPURA	07/2009	421.01 -	994.85	898.22	07/2013 02/2011	08/2015	25	54
102	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19 -	2,743.19	2,659.80	12/2013 -	09/2015	21	-
103	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	487.49	336.42	06/2014 -	09/2015	15	-
104	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	468.60	02/2014 -	09/2015	19	-
105	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,KARNATAKA	03/2005	1,007.16 -	1,007.16	970.31	12/2007 12/2009	12/2015	96	72
106	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,MULTI STATE	09/2012	1,508.74 -	1,508.74	627.18	03/2015 -	12/2015	9	-
107	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 721.81	721.81	515.79	09/2010 06/2013	12/2015	63	30
108	TRANSM SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 -	4,404.57	1,221.75	01/2015 -	12/2015	11	-
109	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	719.74	11/2012 -	12/2015	37	-
110	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 -	752.64	473.82	07/2013 -	12/2015	29	-
111	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	419.81	11/2013 -	12/2015	25	-
112	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATISGARH	01/2012	1,422.85 -	1,422.85	932.12	01/2015 -	12/2015	11	-
113	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATISGARH	03/2012	9,569.76 -	9,569.76	3,874.59	06/2015 -	12/2015	6	-
114	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	478.22	11/2014 -	12/2015	13	-
115	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	664.43	06/2015 -	12/2015	6	-
116	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	2,159.07	1,889.15	09/2008 03/2012	03/2016	90	48
117	PARE HYDRO ELECTRIC PROJECT - [N18000045]NNEEPCO,ARUNACHAL PRADESH	12/2008	573.99 1,487.49	1,487.49	994.41	08/2013 -	03/2016	31	-

(March 2015)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
118	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	458.76	11/2011 -	03/2016	52	-
119	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	313.27	02/2012 -	03/2016	49	-
120	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	4,041.48	10/2012 -	03/2016	41	-
121	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	10,130.80	08/2013 -	03/2016	31	-
122	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	2,036.00	12/2012 -	03/2016	39	-
123	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,045.29	08/2012 -	03/2016	43	-
124	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,170.02	04/2013 -	03/2016	35	-
125	EASTERN REGION STRENGTHENING SCHEME- III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	965.23	11/2012 -	03/2016	40	-
126	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 -	155.57	-	03/2016 -	05/2016	2	-
127	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]NHPC,WEST BENGAL	09/2005	1,061.38 -	1,929.15	1,715.90	09/2009 -	06/2016	81	-
128	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	16.00	09/2014 -	06/2016	21	-
129	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM	07/1998	368.72 1,381.71	1,381.71	800.74	07/2006 12/2015	10/2016	123	10
130	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,497.72	3,915.36	01/2016 -	11/2016	10	-
131	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	7,921.47	3,839.00	09/2016 -	02/2017	5	-
132	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 6,749.18	6,749.18	5,138.00	09/2011 -	03/2017	66	-
133	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	01/2012	15,166.19 -	15,166.19	7,894.00	01/2017 -	03/2017	2	-
134	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH	07/2013	3,363.12 -	3,363.12	510.00	12/2016 -	05/2017	5	-
135	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	4,571.00	11/2016 -	08/2017	9	-
136	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 15,095.67	15,095.67	10,750.00	12/2009 10/2014	03/2018	99	41
137	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	1,189.01	07/2010 02/2016	05/2018	94	27
138	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	2,420.00	03/2013 -	05/2018	62	-
139	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	7,531.72	4,959.80	09/2009 -	12/2018	111	-

(March 2015)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	Total		152,744.08 -	176,411.87	120,344.01				
	<u>RAILWAYS</u>								
140	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	608.02	602.10	03/1994 -	03/2015	252	-
141	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	883.00	755.50	02/2009 -	03/2015	73	-
142	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 393.46	1,026.00	181.48	03/2007 03/2007	03/2015	96	96
143	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	432.72	436.85	12/2009 03/2011	06/2015	66	51
144	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	874.57	703.56	03/2013 -	09/2015	30	-
145	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 -	207.52	223.44	12/2012 -	09/2015	33	-
146	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 245.39	245.39	249.33	12/2008 -	10/2015	82	-
147	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	335.00	230.67	06/2004 -	12/2015	138	-
148	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 -	2,921.00	2,339.60	10/2007 12/2012	12/2015	98	36
149	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	800.00	798.47	03/2010 -	12/2015	69	-
150	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 495.44	1,781.98	420.45	03/2004 12/2010	03/2016	144	63
151	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	272.39	141.55	03/2012 12/2013	03/2016	48	27
152	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	2,069.60	34.87	03/2014 -	03/2016	24	-
153	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM	04/1998	227.90 200.00	331.40	182.22	12/2012 -	03/2016	39	-
154	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 -	5,500.00	4,734.45	03/2009 -	03/2016	84	-
155	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	583.00	144.66	12/2015 -	03/2016	3	-
156	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 575.00	1,242.25	1,005.81	03/2007 -	03/2016	108	-
157	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL,WEST BENGAL	04/2010	2,397.72 -	2,397.72	143.73	03/2016 -	06/2016	3	-
158	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	230.00	68.67	03/2015 -	12/2016	21	-
159	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	714.10	59.18	04/2016 -	03/2017	11	-

(March 2015)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
160	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR, ASSAM	09/1997	1,500.00 1,000.00	4,996.19	3,410.06	04/2008 03/2014	06/2017	110	39
161	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR, BIHAR	09/2001	492.98 -	1,727.27	743.74	12/2010 -	03/2018	87	-
162	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	733.00 733.00	2,531.34	1,732.43	12/2008 -	03/2018	111	-
163	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA	04/2008	813.34 813.34	2,876.00	823.83	03/2014 -	03/2018	48	-
164	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	619.34 619.34	2,820.25	199.31	04/2014 03/2015	03/2018	47	36
165	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP, TELANGANA	04/2012	632.68 -	816.55	42.58	03/2016 -	03/2018	24	-
166	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	19,565.00	10,658.34	11/2002 -	12/2018	193	-
167	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR	04/2003	727.56 727.56	6,570.75	2,787.99	03/2011 03/2014	03/2019	96	60
168	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, MULTI STATE	02/1997	386.30 1,157.54	1,544.40	590.26	03/1998 -	12/2019	261	-
169	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	2,371.85	486.25	03/2005 12/2008	12/2019	177	132
170	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97 1,013.74	1,428.00	466.36	06/2005 07/2011	12/2019	174	101
171	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48 1,339.48	4,190.00	88.56	12/2015 -	03/2020	51	-
	Total		22,617.11 -	74,893.26	35,486.30				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
172	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, ASSAM	12/2003	157.47 157.47	154.57	268.50	09/2007 03/2014	03/2015	90	12
173	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, UTTAR PRADESH	12/2003	155.00 -	201.66	191.80	09/2008 -	03/2015	78	-
174	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, ASSAM	12/2003	264.72 -	264.72	315.90	06/2008 -	03/2015	81	-
175	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, ASSAM	12/2003	198.16 -	198.16	345.80	04/2008 01/2015	03/2015	83	2
176	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI, ASSAM	12/2003	200.00 -	200.00	290.00	06/2008 -	03/2015	81	-
177	JAIPUR-TONK-DEOLI - [N24000135]NHAI, RAJASTHAN	06/2010	792.06 -	792.06	1,983.00	12/2012 -	03/2015	27	-
178	HAZARIBAGH-RANCHI - [N24000141]NHAI, JHARKHAND	08/2010	625.07 -	625.07	995.90	01/2013 -	03/2015	26	-
179	MURADABAD-BAREILY - [N24000154]NHAI, UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,425.00	06/2013 -	03/2015	21	-
180	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI, MULTI STATE	02/2011	2,498.76 -	2,498.76	-	08/2014 -	03/2015	7	-
181	PATNA-MUZZAFFARPUR - [N24000165]NHAI, BIHAR	08/2010	671.30 -	671.30	632.70	02/2013 -	03/2015	25	-

(March 2015)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
182	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	535.00	52.18	12/2013 -	03/2015	15	-
183	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	381.50	06/2013 -	03/2015	21	-
184	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	759.90	01/2014 -	03/2015	14	-
185	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	408.10	04/2014 -	03/2015	11	-
186	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	835.00	476.40	01/2014 -	03/2015	14	-
187	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	500.29	633.30	08/2013 -	03/2015	19	-
188	SAMBALPUR-BARGARH- CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	909.00	982.90	05/2014 -	03/2015	10	-
189	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	267.81	699.60	02/2013 -	03/2015	25	-
190	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19 -	484.19	285.50	10/2014 -	03/2015	5	-
191	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	356.40	-	07/2014 -	03/2015	8	-
192	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH	10/2012	250.50 -	250.50	65.26	10/2014 -	03/2015	5	-
193	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	373.47	28.51	07/2014 -	03/2015	8	-
194	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT	03/2012	828.00 -	828.00	52.01	09/2014 -	03/2015	6	-
195	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN	03/2012	333.51 -	333.51	152.50	09/2014 -	03/2015	6	-
196	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	495.40	12/2009 -	04/2015	64	-
197	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	250.39	285.30	10/2008 -	05/2015	79	-
198	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,374.00	12/2013 -	05/2015	17	-
199	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	148.80	05/2013 -	05/2015	24	-
200	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	1,179.00	11/2013 -	05/2015	18	-
201	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	385.13	159.20	04/2009 -	06/2015	74	-
202	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	167.64	180.30	11/2008 -	06/2015	79	-
203	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	280.13	173.80	11/2008 -	06/2015	79	-
204	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	200.00	207.60	04/2009 -	06/2015	74	-

(March 2015)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
205	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	332.94	550.30	09/2008 -	06/2015	81	-
206	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	331.23	242.10	07/2009 -	06/2015	71	-
207	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	465.50	322.70	09/2007 -	06/2015	93	-
208	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	667.10	05/2010 -	06/2015	61	-
209	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	572.30	886.90	10/2011 -	06/2015	44	-
210	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	650.00	1,178.00	11/2013 -	06/2015	19	-
211	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	1,141.00	2,445.00	08/2013 -	06/2015	22	-
212	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	942.90	07/2013 -	06/2015	23	-
213	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	624.00	333.72	04/2014 -	07/2015	15	-
214	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	195.00	280.30	06/2008 -	08/2015	86	-
215	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	237.80	328.60	06/2008 -	09/2015	87	-
216	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	795.00	1,133.00	05/2012 -	09/2015	40	-
217	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	1,173.00	07/2013 -	09/2015	26	-
218	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	398.00	462.00	02/2014 -	09/2015	19	-
219	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	664.00	776.40	02/2014 -	10/2015	20	-
220	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	1,509.10	2,686.00	09/2012 -	11/2015	38	-
221	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	11/2015	48	-
222	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	574.00	991.70	03/2014 -	11/2015	20	-
223	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	2,388.00	2,301.00	06/2014 -	11/2015	17	-
224	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	682.00	752.70	10/2013 -	11/2015	25	-
225	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	230.00	251.50	06/2005 -	12/2015	126	-
226	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	361.00	366.80	02/2009 -	12/2015	82	-
227	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	208.00	334.80	04/2008 04/2015	12/2015	92	8
228	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 -	212.00	127.10	09/2007 -	12/2015	99	-

(March 2015)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
229	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	232.45	317.70	09/2010 -	12/2015	63	-
230	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	12/2015	32	-
231	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	901.60	03/2013 -	12/2015	33	-
232	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	996.80	05/2013 -	12/2015	31	-
233	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,292.00	03/2013 -	12/2015	33	-
234	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	325.00	611.80	05/2013 -	12/2015	31	-
235	2 LANING OF DINDIGUL - PERIGULAM THENI-KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	363.00	08/2013 -	12/2015	28	-
236	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	805.39	842.20	03/2013 -	12/2015	33	-
237	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	2,188.00	05/2014 -	12/2015	19	-
238	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	835.60	07/2013 -	12/2015	29	-
239	SRINAGAR TO BANIHAI - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	323.00	06/2014 -	12/2015	18	-
240	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	209.00	38.77	01/2013 -	12/2015	35	-
241	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	4,030.00	09/2013 -	12/2015	27	-
242	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	593.50	03/2013 -	12/2015	33	-
243	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	1,047.00	295.70	06/2014 -	12/2015	18	-
244	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	1,396.18	1,934.00	09/2014 -	12/2015	15	-
245	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	141.30	01/2014 -	12/2015	23	-
246	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	478.00	328.70	10/2013 -	12/2015	26	-
247	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	942.69	286.80	06/2014 -	12/2015	18	-
248	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00 -	1,232.00	87.61	08/2015 -	02/2016	6	-
249	SIX LANNING OF VADAKKANANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	156.90	08/2012 -	03/2016	43	-
250	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	-	10/2013 -	03/2016	29	-
251	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	593.00	761.30	07/2013 -	04/2016	33	-
252	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	1,928.22	647.40	04/2015 -	04/2016	12	-

(March 2015)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
253	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	353.37	446.20	10/2011 -	06/2016	56	-
254	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,170.00	07/2015 -	06/2016	11	-
255	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	2,159.00	622.70	06/2015 -	06/2016	12	-
256	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	929.60	09/2014 -	06/2016	21	-
257	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,MULTI STATE	12/2012	1,479.00 -	1,479.00	368.60	06/2015 -	06/2016	12	-
258	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	1,078.84	1,922.00	08/2013 -	08/2016	36	-
259	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	588.40	02/2014 -	08/2016	30	-
260	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	1,655.00	655.20	09/2013 -	11/2016	38	-
261	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	193.45	66.11	11/2012 -	12/2016	49	-
262	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	39.55	09/2013 -	12/2016	39	-
263	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2016	35	-
264	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	281.31	180.10	02/2010 -	02/2017	84	-
265	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	726.40	07/2014 -	02/2017	31	-
266	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	1,287.95	540.40	11/2015 -	03/2017	16	-
267	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,138.00	03/2014 -	04/2017	37	-
268	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	580.43	450.70	08/2013 -	05/2017	45	-
269	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	998.79	1,610.00	08/2013 -	07/2017	47	-
270	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	867.00	598.60	02/2015 -	12/2017	34	-
	Total		76,018.50 -	77,867.94	70,031.82				
	<u>TELECOMMUNICATIONS</u>								
271	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL,ASSAM	06/2007	336.81 -	336.81	195.94	01/2009 -	03/2015	74	-
272	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	384.00	54.97	10/2010 08/2015	09/2015	59	1
	Total		720.81 -	720.81	250.91				
	<u>URBAN DEVELOPMENT</u>								

(March 2015)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
273	C/O MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB - [N28000070]CPWD,PUNJAB	08/2005	191.24 -	191.24	9.91	08/2007 -	03/2015	91	-
274	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	205.00	97.61	03/2012 -	04/2015	37	-
275	FARIDABAD EXTENSION - [N28000057]DMRCL,DELHI	09/2011	2,494.00 -	2,494.00	1,164.03	09/2014 -	05/2015	8	-
276	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD,WEST BENGAL	01/2009	225.81 -	225.81	17.60	06/2012 -	06/2015	36	-
277	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD,ODISHA	11/2012	238.43 -	238.43	-	02/2015 -	08/2015	6	-
278	C/O NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 -	315.00	88.54	06/2015 -	08/2015	2	-
279	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	24.71	11/2014 -	10/2015	11	-
280	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85 -	261.85	131.77	05/2013 -	11/2015	30	-
281	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	12/2015	11	-
282	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI	05/2012	405.01 -	405.01	-	12/2014 -	04/2016	16	-
283	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	-	03/2016 -	05/2016	2	-
284	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	-	09/2015 -	07/2016	10	-
285	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 -	14,600.00	-	12/2015 -	08/2016	8	-
286	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	38,585.00	14,321.39	03/2016 -	12/2016	9	-
287	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	188.87	24.44	12/2014 -	12/2016	24	-
288	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	332.72	0.11	09/2016 -	12/2016	3	-
289	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	884.30	103.45	08/2014 -	06/2017	34	-
	Total		82,662.49 -	82,662.49	15,983.56				
	Grand Total		503,581.88	611,931.57	382,550.11				
