

दलनह; {k= dh ifj; k t ukv k
CENTRAL SECTOR PROJECTS

₹150 djkM vkj vf/kd ykxr okyh

(₹ 150 Crore and above)

361ohi ¶Yk'k fjikVl@361st Flash Report

uoEcj] 2015@November, 2015



Hkkjr ljdkj / **Government of India**

lkf[;dh vkj dk;lØe dk;kUo;u e=k;y ;

Ministry of Statistics and Programme Implementation

vk/kkjh ljpuk vkj ifj;ktuk i;ck/ku iHkkx
Infrastructure and Project Monitoring Division

ljnkj iV;y Hkou] lln ekx;

Sardar Patel Bhavan, Sansad Marg,

ubl fnYyh / **New Delhi-110001**

oC lkbV / **Website- www.cspm.gov.in**

Abbreviations used in the report

AAI	Airport Authority of India Ltd.
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead Travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised Catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Operation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petroleum Corporation Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative Ltd.
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation Ltd.
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Corporation.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Corporation.
NCL	Northern Coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation Ltd.
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corporation Ltd.
NGN	Next Generation Network
NLC	Neyveli Lignite Corporation Ltd.
NMDC	National Mineral Development Corporation Ltd.
NPC	Nuclear Power Corporation Ltd.
NRL	Numaligarh Refinery Ltd.
OB	Over Burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over Bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India Ltd.
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

Contents	
	Pages
Executive Summary Hindi	1-19
Executive Summary English	20-36
Month wise List of Completed Projects Costing Rs. 150 crore and above during 2015-2016	37-40
Month wise List of Deleted Projects Costing Rs. 150 crore and above during 2015-2016	41-42
Summary of projects	43-57
Graphical Presentation of All Projects	58-70
Sector wise Analysis of Projects	71-108
Sector wise Graph	109-120
Annexures	121-121
Status of central sector projects costing Rs.150 Crore and above	122-122
List of projects in which expenditure is more than approved cost	123-129
Details of Projects Ahead of Schedule w.r.t. Original Schedule	130-130
Details of On Schedule Projects w.r.t. Original Schedule	131-138
Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule	139-150
Details of Delayed Projects w.r.t. Original and Revised Schedule	151-172
Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule	173-176
Details of Projects Without Date of Commissioning	177-193
Details of projects without original Date of Commissioning	194-195
Details of projects without Milestones w.r.t. original schedule	196-219
List of Projects Ahead of Schedule w.r.t. Latest Schedule	220-221
List of Projects on schedule w.r.t. Latest Schedule	222-231
List of ongoing projects having cost overrun w.r.t. to revised schedule	232-241
List of Delayed Projects w.r.t. Latest Schedule	242-251
Details of Central Sector Projects Showing Time overruns of 6 Months and More	252-261
Details of Central Sector Projects Showing Cost overruns of More Than Rs. 100 Crore	262-270
Details Of Central Sector Projects Showing Time Overruns Of 6 Months and More and cost overruns of Rs. 100 Crore	271-275

कार्यकारी सारांश

1. नवंबर, 2015 की फ्लैश रिपोर्ट में ₹ 150 करोड़ और उससे अधिक लागत वाली केन्द्रीय क्षेत्र की 787 अवसंरचनात्मक परियोजनाओं की स्थिति दी गई है। नवंबर 2015 के दौरान, विद्युत क्षेत्र की 1 परियोजना के पूरा होने की सूचना दी गई है।

2. संदर्भाधीन माह के दौरान, 787 परियोजनाओं में से, 208 परियोजनाओं में मूल समय-सारणी की तुलना में विलंब हुआ तथा 35 परियोजनाओं के संबंध में पिछले माह में सूचित की गई समापन की तारीख की तुलना में अतिरिक्त विलंब की सूचना दी गई है। इन 35 परियोजनाओं में से, 20 परियोजनाएं ₹1000 करोड़ और अधिक लागत वाली बड़ी परियोजनाएं हैं।

क्र.सं.	क्षेत्र	निगरानी के तहत आने वाली परियोजनाएं (सं.)	मूल समय-सारणी की तुलना में विलंबित परियोजनाएं (सं.)	रिपोर्ट वाले माह के दौरान अतिरिक्त विलंबित परियोजनाएं (सं.)	अतिरिक्त विलंबित बड़ी परियोजनाएं (सं.)
1.	रेलवे	296	27	0	0
2.	सड़क परिवहन एवं राजमार्ग	163	9	1	0
3.	विद्युत	105	57	18	15
4.	कोयला	81	43	1	0
5.	पेट्रोलियम	63	37	10	3
6.	शहरी विकास	31	12	1	0
7.	इस्पात	22	10	3	1
8.	नागर विमानन	5	1	0	0
9.	पोत परिवहन एवं पत्तन	6	4	0	0
10.	स्वास्थ्य और परिवार कल्याण	5	1	0	0
11.	परमाणु ऊर्जा	4	4	1	1
12.	दूरसंचार	2	1	0	0
13.	उर्वरक	1	0	0	0
14.	खान	1	0	0	0
15.	पेट्रोसायन	1	1	0	0
16.	भारी उद्योग	1	1	0	0
कुल		787	208	35	20

3. 787 परियोजनाओं के कार्यान्वयन की कुल मूल लागत ₹10,20,904.25 करोड़ थी तथा उनके पूरा होने की अनुमानित लागत ₹12,32,092.39 करोड़ होने की संभावना है, जो ₹2,11,188.14 करोड़ (मूल लागत का 20.69%) की समग्र लागत वृद्धि को दर्शाता है। नवंबर, 2015 तक इन परियोजनाओं पर किया गया व्यय ₹4,85,200.10 करोड़ है, जो परियोजनाओं की अनुमानित लागत का 39.38% है।

लागतवृद्धि की अधिकतम प्रतिशतता वाली परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई हैं:-

**लागतवृद्धि की अधिकतम प्रतिशतता वाली (अधिकतम संख्या में पांच) परियोजनाओं की क्षेत्र-वार सूची
(30.11.2015 की स्थिति के अनुसार)**

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (करोड़ ₹.)	अनुमानित लागत(करोड़ ₹.)	लागत वृद्धि(%)
परमाणु ऊर्जा					
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	13171.00	22462.00	70.54
2	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर (भाविनि, 500 एमडब्ल्यूई)	09/2003	3492.00	5677.00	62.57
नागर विमानन					
1	विभिन्न हवाई अड्डों पर सं.56 एनओएस एयरफील्ड फायर निविदाओं की आपूर्ति	10/2012	217.60	244.10	12.18
कोयला					
1	अदरियाला शाफ्ट परियोजना	12/2009	212.34	1228.39	478.50
2	निगाही ओसी विस्तार परियोजना 10 एमटीवाई से 15 एमटीवाई, सिंगरौली	10/2007	259.40	486.57	87.58
3	अमलाई ओसी विस्तार, सेक्टर-बी (1.50 एमटीवाई)	11/2009	150.59	198.59	31.87
4	मनुगुरु ओसी परियोजना का आरएफआर	11/2012	430.45	486.27	12.97
5	हिंगुला ओसी-II विस्तार फेज-III (15 एमटीवाई)	11/2008	479.53	479.63	0.02
भारी उद्योग					
1	राष्ट्रीय औटोमोटिव टेस्टिंग तथा आरडी अवसंरचना परियोजना (एनएटीआरआईपी)	04/2011	1718.00	3827.30	122.78
पेट्रोरसायन					
1	असम गैस क्रैकर प्रोजेक्ट	04/2006	5460.61	9965.00	82.49
पेट्रोलियम					
1	पादुर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	993.00	1693.00	70.49
2	मंगलौर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	732.00	1227.00	67.62
3	कोरबा में विपणन टीओपी	01/2011	141.86	232.00	63.54

4	उरान चाकन/शिकरापुर एलपीजी पाइपलाइन	12/2009	309.81	462.79	49.38
5	रिग सागर सम्राट से मोबाइल ऑफशोर प्रोडक्शन यूनिट (एमओपीएस) का रूपांतरण	03/2011	861.79	1256.72	45.83
विद्युत					
1	तुरीअल जल विद्युत परियोजना (60 मेगा.)	07/1998	368.72	1381.71	274.73
2	सुबनसिरी लोअर एच.ई.पी. (8X250 मेगा.) (एनएचपीसी))	09/2003	6285.33	18063.89	187.40
3	कामेंग जल विद्युत परियोजना (नीपको)	12/2004	2496.90	6476.34	159.38
4	पारे जल विद्युत परियोजना	12/2008	573.99	1487.49	159.15
5	त्रिपुरा गैस आधारित विद्युत परियोजना	07/2009	421.01	1007.57	139.32
रेलवे					
1	इकलाखी-बालुरघाट सहित गाजोल-इटाहार से नई बीजी रेलवे लाइन (एनएल), एनईएफआर	04/1983	36.80	1336.57	3531.98
2	बांकुरा-दामोदर (जीसी) (एसईआर)	03/1998	111.90	2371.85	2019.62
3	अकोला-खांडवा जीसी अकोला-अकोट	04/2008	184.26	2000.00	985.42
4	बंगलौर-सत्यमंगलम (एनएल) (एसडब्ल्यूआर)	04/1996	138.00	1382.78	902.01
5	तिरुचिरापल्लई-नागोरे-करायकल (एसआर) (जीसी)	09/1995	100.00	980.00	880.00
सड़क परिवहन एवं राजमार्ग					
1	पानीपत-जालंधर छः लेन (96 किमी. से 387.1 किमी.)	05/2009	1108.00	2288.00	106.50
2	मैबंग से लुमडिंग (एएस-25), 83.400 किमी. से 111.000 किमी.	12/2003	199.81	385.13	92.75
3	मैबंग से लुमडिंग (एएस-24) 111.000 किमी. से 126.450 किमी.	12/2003	155.04	280.13	80.68
4	हरंगाजो से मैबंग, एनएच-54	12/2003	196.00	331.23	68.99
5	एनडब्ल्यूई एस के तहत एनएच-202 पर अप्रोच रोड सहित वेंकटपुरम के समीप गोदावरी नदी पुल का निर्माण	03/2011	218.31	339.82	55.66
पोत परिवहन एवं पत्तन					
1	एन्नोर मनाली एक्सप्रेस वे, एफ/ओ स्पेशल परपस वेहिकल (एसपीवी)	10/2002	150.00	600.00	300.00

2	मुंबई में ऑफशोर कंटेनर बर्थ का निर्माण तथा बीओटी आधार पर कंटेनर टर्मिनल का विकास	01/2007	366.39	669.46	82.72
3	कोचीन पोर्ट्स के बल्लापाड़म में आसीटीटी के लिए रेल कनेक्टिविटी	03/2007	245.67	409.83	66.82
4	2 ऑफशोर कंटेनर बर्थ और टर्मिनल का निर्माण और विकास	11/2007	1228.00	1460.00	18.89
इस्पात					
1	सिंटर मशीनों - 1 और 2 की सुधार	12/2009	343.00	488.40	42.39
शहरी विकास					
1	बंगलौर मेट्रो रेल परियोजना	05/2006	6395.00	11609.00	81.53

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

4. पूर्ण रूप से अधिकतम लागतवृद्धि (सीओआर) वाली (अधिकतम संख्या में पांच) परियोजनाओं की क्षेत्र-वार सूची इस प्रकार है:-

**अधिकतम लागतवृद्धि (सीओआर) वाली (अधिकतम संख्या में 5) परियोजनाओं की क्षेत्र-वार सूची
(30.11.2015 की स्थिति के अनुसार)**

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (रु. करोड़ में)	अनुमानित लागत (रु. करोड़ में)	लागतवृद्धि (रु. करोड़ में)
परमाणु ऊर्जा					
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	13171.00	22462.00	9291.00
2	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर (भाविनि, 500 एमडब्ल्यूई)	09/2003	3492.00	5677.00	2185.00
नागर विमानन					
1	विभिन्न हवाई अड्डों पर सं.56 एयरफील्ड फायर निविदाओं की आपूर्ति	10/2012	217.60	244.10	26.50
कोयला					
1	अदरियाला शाफ्ट परियोजना	12/2009	212.34	1228.39	1016.05
2	निगाही ओसी विस्तार परियोजना 10 एमटीवाई से 15 एमटीवाई, सिंगरौली	10/2007	259.40	486.57	227.17
3	अमलाई ओसी विस्तार, सेक्टर-बी (1.50	11/2012	430.45	486.27	55.82

	एमटीवाई)				
4	मनुगुरु ओसी परियोजनाओं के आरएफआर	11/2009	150.59	198.59	48.00
5	हिंगुला ओसी-II विस्तार फेज-III (15 एमटीवाई)	11/2008	479.53	479.63	0.10
भारी उद्योग					
1	राष्ट्रीय औटोमोटिव टेस्टिंग तथा आरडी अवसंरचना परियोजना (एनएटीआरआईपी)	04/2011	1718.00	3827.30	2109.30
पेट्रोसायन					
1	असम गैस क्रैकर परियोजना	04/2006	5460.61	9965.00	4504.39
पेट्रोलियम					
1	पारादीप रिफाइनरी परियोजना	02/2009	29777.00	34555.00	4778.00
2	समेकित रिफाइनरी विस्तार परियोजना	03/2012	14225.00	16504.00	2279.00
3	बेसिन क्षेत्र का एकीकृत विकास	12/2012	3513.07	4619.94	1106.87
4	वशिष्टा तथा एस-1 क्षेत्रों का समेकित विकास	05/2013	4124.35	4941.49	817.14
5	पादुर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	993.00	1693.00	700.00
विद्युत					
1	सुबनसिरी लोअर एच.ई.पी. (8X250 मेगावाट) (एनएचपीसी)	09/2003	6285.33	18063.89	11778.56
2	बाढ़ एसटीपीपी (3X660मेगावाट) एनटीपीसी	02/2005	8692.97	15095.67	6402.70
3	रघुनाथपुर थर्मल पावर स्टेशन फेज-I	04/2007	4122.00	9606.82	5484.82
4	कामेंग जल विद्युत परियोजना (नीपको)	12/2004	2496.90	6476.34	3979.44
5	पार्वती एचईपी (4x200 मेवा.) (एनएचपीसी) II	09/2002	3919.59	7818.68	3899.09
रेलवे					
1	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	03/1995	2500.00	19565.00	17065.00
2	जिरिबाम से इम्फाल (तुपुई)(एनएल)(एनईएफआर)	04/2003	727.56	6570.75	5843.19
3	लुमडिंग-सिलचर जिरिबाम, बदरपुर-बराईग्राम कुमारघाट राष्ट्रीय परियोजना	04/1996	1676.31	5500.00	3823.69
4	बोगीबिल तथा लिंक लाइन पर ब्रह्मपुत्र पुल, एनईएफआर	09/1997	1500.00	4996.19	3496.19
5	सीवोक रंगपो, एनईएफआर	04/2008	1339.48	4190.00	2850.52

सड़क परिवहन एवं राजमार्ग					
1	पानीपत-जालंधर 6 लेन (96 किमी. से 387.1 किमी.	05/2009	1108.00	2288.00	1180.00
2	मैबंग से लुमडिंग (एएस-25), 83.400 किमी. से 111.000 किमी.	12/2003	199.81	385.13	185.32
3	हरंगाजो से मैबंग, एनएच-54	12/2003	196.00	331.23	135.23
4	मैबंग से लुमडिंग, (एएस-24) 111.000 किमी. से 126.450 किमी. एनएच-54	12/2003	155.04	280.13	125.09
5	एलडब्ल्यूई एस के तहत एनएच-202 पर अप्रोच रोड सहित वैकटपुरम के समीप गोदावरी नदी पुल का निर्माण	03/2011	218.31	339.82	121.51
पोत परिवहन एवं पत्तन					
1	एन्नोर मनाली एक्सप्रेस वे, एफ/ओ स्पेशल परपस वेहिकल (एसपीवी)	10/2002	150.00	600.00	450.00
2	मुंबई में ऑफशोर कंटेनर बर्थ का निर्माण तथा बीओटी आधार पर कंटेनर टर्मिनल का विकास	01/2007	366.39	669.46	303.07
3	2 ऑफशोर कंटेनर बर्थ और टर्मिनल का निर्माण और विकास	11/2007	1228.00	1460.00	232.00
4	कोचीन पोर्ट्स के बल्लापाइम में आईसीटीटी के लिए रेल कनेक्टिविटी	03/2007	245.67	409.83	164.16
इस्पात					
1	सिंटर मंशीन -1 और 2 का सुधार	12/2009	343.00	488.40	145.40
शहरी विकास					
1	बंगलौर मेट्रो रेल परियोजना	05/2006	6395.00	11609.00	5214.00

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

5. 787 परियोजनाओं में से, 7 परियोजनाएं समय से पहले चल रही हैं, 146 समय पर तथा 208 परियोजनाएं मूल समय-सारणी की तुलना में विलंबित हैं । तथापि, विलंबित परियोजनाओं की संख्या में 174 तक की कमी हो जाती है यदि विलंब की गणना समापन की अद्यतन समय-सारणी के आधार पर की जाती है । इसके अलावा, 30 परियोजनाएं किसी आरंभ संबंधी समय-सारणी/तारीख के बिना स्वीकृत की गई हैं तथा 396 परियोजनाओं के संबंध में न तो शुरू करने का वर्ष और न परियोजना के अनंतिम रूप से पूरा होने की अवधि सूचित की गई है । 208 विलंबित परियोजनाओं में से, 35 परियोजनाओं में 1 से 12 माह तक का विलंब हुआ, 49 परियोजनाओं में 13 से 24 महीने तक का विलंब हुआ, 73 परियोजनाओं में

25 से 60 माह तक का विलंब हुआ तथा 51 परियोजनाओं में 61 माह और उससे अधिक का विलंब हुआ । अधिकतम समयवृद्धि (टीओआर) वाली परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई हैं:-

**अधिकतम समयवृद्धि (टीओआर) वाली (अधिकतम संख्या में 5) परियोजनाओं की क्षेत्र-वार सूची
(30.11.2015 की स्थिति के अनुसार)**

क्र.सं.	परियोजना	अनुमोदन की तारीख	शुरू करने की मूल तारीख	शुरू करने की अनुमानित तारीख	समय वृद्धि (महीना)
परमाणु ऊर्जा					
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	12/2008	06/2016	90
2	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर (भाविनि, 500 एमडब्ल्यूई)	09/2003	09/2010	09/2016	72
3	काकरापार परमाणु ऊर्जा परियोजना-3 और 4	10/2009	12/2015	10/2017	22
4	राजस्थान परमाणु ऊर्जा परियोजना-7 और 8 (2x700 मेवा)	10/2009	12/2016	05/2018	17
नागर विमानन					
1	पाकयांग (सिक्किम) हवाई अड्डा में नए हवाई अड्डे का निर्माण	01/2009	01/2011	09/2017	80
कोयला					
1	मगध ओसी 20 एमटीवाई (सीसीएल)	08/2008	07/2012	03/2021	104
2	बलराम ओसीपी विस्तार, एमसीएल 8.00 एमटीवाई	12/2007	03/2010	03/2017	84
3	कुल्दा ओसीपी (महानदी कोल्डफील्ड लिमि.)	01/2005	03/2010	03/2016	72
4	अशोक विस्तार ओसीपी सीसीएल (10 एमटीवाई)	12/2007	03/2011	03/2017	72
5	झंझरा आर-VI सीम पीएसएलडब्ल्यू	11/2006	03/2011	03/2017	72
स्वास्थ्य और परिवार कल्याण					
1	एलजीबीआरआईएमएच-तेजपुर, असम	07/2012	12/2014	03/2016	15
भारी उद्योग					
1	राष्ट्रीय औटोमोटिव टेस्टिंग तथा आरडी अवसंरचना परियोजना (एनएटीआरआईपी)	04/2011	09/2011	12/2017	75
पेट्रोरसायन					
1	असम गैस क्रैकर परियोजना	04/2006	04/2012	12/2015	44
पेट्रोलियम					
1	फुलपुर-हल्दिया पाइपलाइन परियोजना चरण-I	07/2009	01/2013	12/2018	71
2	वीकेपीएल उन्नयन तथा स्परलाइन को बिछाना (भिलवाड़ा तथा चितौड़गढ़ के लिए)	12/2009	06/2011	03/2016	57
3	12 ऑफशोर आपूर्ति उपकरणों का निर्माण (ओएसवी)	06/2007	09/2011	06/2016	57

4	मंगलौर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	10/2011	03/2016	53
5	पादुर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	01/2012	03/2016	50
विद्युत					
1	तुरीअल जल विद्युत परियोजना (60 मेगावाट)	07/1998	07/2006	10/2017	135
2	पार्वती एचईपी (4X200 मेगावाट) (एनएचपीसी) II	09/2002	09/2009	12/2018	111
3	बाढ़ एसटीपीपी (3X660 मेवा) एनटीपीसी	02/2005	01/2011	05/2018	88
4	कामेंग जल विद्युत परियोजना (नीपको)	12/2004	12/2009	12/2016	84
5	तीस्ता लो डैम एचईपी, स्टेज-IV (4X40 मेवा) (एनएचपीसी)	09/2005	09/2009	06/2016	81
रेलवे					
1	गोंडिया-जबलपुर (जीसी), (एसईसीआर)	02/1997	03/1998	12/2019	261
2	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	03/1995	11/2002	12/2018	193
3	बांकुरा-दामोदर (जीसी) (एसईआर)	03/1998	03/2005	12/2019	177
4	तमलुक-दीघा लाइन दोहरीकरण, (एसईआर)	03/1984	06/2005	12/2019	174
5	बेलापुर-सीवुड-उरान विद्युतीकृत दोहरी लाइन (एमटीपी)	03/1996	03/2004	03/2016	144
सड़क परिवहन एवं राजमार्ग					
1	नलबारी से बिजनी (एएस-7)	12/2003	04/2008	01/2017	105
2	सोनापुर से गुवाहाटी से (एएस-3)	12/2003	03/2008	04/2016	97
3	नलबारी से बिजनी (एएस-6)	12/2003	06/2008	04/2016	94
4	गुवाहाटी से नलबारी (एएस-4)	12/2003	04/2008	12/2015	92
5	गुवाहाटी से नलबारी (एएस-5)	12/2003	04/2008	12/2015	92
पोत परिवहन एवं पत्तन					
1	एन्नोर मनाली एक्सप्रेस वे, एफ/ओ स्पेशल परपस वेहिकल (एसपीवी)	10/2002	03/2006	12/2015	117
2	कोचीन पोर्ट्स के बल्लापाइम में आईसीटीटी के लिए रेल कनेक्टिविटी	03/2007	04/2009	08/2016	88
3	2 ऑफशोर कंटेनर बर्थ और टर्मिनल का निर्माण और विकास	11/2007	12/2010	09/2017	81
4	मुंबई में ऑफशोर कंटेनर बर्थ का निर्माण तथा बीओटी आधार पर कंटेनर टर्मिनल का विकास	01/2007	12/2010	01/2016	61
इस्पात					
1	भिलाई इस्पात संयंत्र का विस्तार	08/2010	03/2013	06/2016	39
2	45 एमवीए साफ्ट से जुड़े दूसरी सुविधाओं की स्थापना	12/2011	10/2013	03/2016	29
3	एसएमएस -1 कन्वर्टर्स सुधार	05/2012	07/2015	03/2017	20
4	एनडीएमसी एकीकृत इस्पात संयंत्र	01/2010	05/2015	12/2016	19
5	बीएसपी, भिलाई, छत्तीसगढ़ में कोक ओवन बैटरी-9 का कोल्ड रिपेयर	07/2012	08/2014	01/2016	17

दूरसंचार					
1	टर्नकी आधार पर बीएसएनएल में ईआरपी कार्यान्वयन	10/2009	10/2010	11/2015	61
शहरी विकास					
1	आईआईएसईआर कोलकाता के लिए हरिघंटा कल्याणी प.बं. में शैक्षिक सहित आवासीय परिसर	01/2009	06/2012	12/2015	42
2	संसदीय सौध संसद भवन परिसर नई दिल्ली में भवन के विस्तार हेतु निर्माण कार्य	05/2009	05/2013	06/2016	37
3	सेंट्रल एकेडमी पुलिस ट्रेनिंग (सीएपीटी) भोपाल का निर्माण	12/2012	12/2014	12/2016	24
4	प्रगति मैदान से जुड़े भूमि में भारत के उच्चतम न्यायालय के लिए अतिरिक्त परिसर का निर्माण	07/2012	08/2014	01/2016	17
5	कामंड में आईआईटी मंडी के लिए फेज I नॉर्थ के तहत विभिन्न भवन	11/2012	11/2014	03/2016	16

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और अधिक समयवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

6. अप्रैल 2015 में, इस मंत्रालय की निगरानी पर चल रहे 758 परियोजनाओं में से, 231 परियोजनाओं के संबंध में लागतवृद्धि तथा 323 परियोजनाओं के संबंध में समयवृद्धि की सूचना प्राप्त हुई है; जबकि नवंबर 2015 के दौरान, 787 परियोजनाओं में से 228 परियोजनाओं के संबंध में लागतवृद्धि तथा 208 परियोजनाओं के संबंध में समयवृद्धि की सूचना प्राप्त हुई है। अप्रैल 2015 की तुलना में, लागतवृद्धि दर्शाने वाली परियोजनाओं की संख्या 30.47% से घटकर 28.97% हो गई, जबकि समयवृद्धि दर्शाने वाली परियोजनाओं के संबंध में 42.61% से घटकर 26.43% हो गई है ।

7. विभिन्न अन्य परियोजना कार्यान्वयन एजेंसियों द्वारा यथा सूचित समयवृद्धि के संक्षिप्त कारणों में भूमि अधिग्रहण में विलंब, वन संबंधी अनुमति में विलंब, उपस्करों की आपूर्ति में विलंब, निधि की कमी, भूवैज्ञानिक गतिविधियां, उपस्कर स्थापित करने में समस्या, भूखनन की स्थिति, सिविल कार्यों में धीमी प्रगति, श्रम की कमी, ठेकेदार द्वारा अपर्याप्त संसाधन जुटाना, माओवादी समस्याएं, न्यायालय मामले, संविदात्मक मुद्दे, आरओयू/आरओडब्ल्यू समस्याएं, कानून और व्यवस्था की स्थिति, आदि शामिल हैं ।

8. मंत्रालय के ऑनलाइन कम्प्यूटरीकृत मॉनीटरिंग सिस्टम (ओसीएमएस) में विभिन्न अवसंरचना परियोजनाओं के लक्ष्यों की निगरानी की परिकल्पना की गई है । परियोजना प्राधिकारियों से नियमित रूप से अनुरोध किया गया है कि वे बेहतर निगरानी को सुचारु बनाने के लिए प्रत्येक परियोजना के संबंध में उपलब्धियों की सूची की प्रविष्टि करें । तथापि, सभी परियोजना एजेंसियां उपलब्धियों की सूची

प्रदान नहीं कर रही हैं। बिना उपलब्धियों वाली पहले की परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई है:-

बिना उपलब्धियों वाली पहले की (सबसे पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची (30.11.2015 की स्थिति के अनुसार)

क्र. सं.	परियोजनाएं	अनुमोदन की तारीख	मूल लागत (करोड़ रु.)	अनुमानित लागत (करोड़ रु.)	संचयी व्यय (करोड़ रु.)	शुरू करने की मूल तारीख	शुरू करने की अनुमानित तारीख
नागर विमानन							
1	पाकयांग (सिक्किम) हवाई अड्डा में नया हवाई अड्डा का निर्माण	01/2009	309.46	309.46	404.81	01/2011	09/2017
2	10 हवाई अड्डों में एयरपोर्ट संचालन नियंत्रण केन्द्रों की स्थापना	02/2010	344.28	344.28	80.60	03/2014	05/2015
3	नई अंतरराष्ट्रीय टर्मिनल भवन का निर्माण, गोवा	05/2010	335.61	318.00	305.01	05/2012	03/2015
4	विभिन्न हवाई अड्डों पर सं. 56 एयरफील्ड फायर टैंडर की आपूर्ति	10/2012	217.60	244.10	30.66	03/2015	09/2015
5	वीएसआई एयरपोर्ट पर नई एकीकृत टर्मिनल भवन का निर्माण	10/2013	314.61	314.61	18.02	एन.ए.	09/2018
कोयला							
1	दुर्गापुर ओसीपी	02/2015	916.24	916.24	0.00	03/2023	03/2023
2	आमगांव ओसी आरसीई	07/2015	316.10	316.10	15.85	03/2020	03/2020
3	बतूरा एच/डब्ल्यू प्रोजेक्ट	07/2015	231.92	231.92	0.00	03/2022	03/2022
उर्वरक							
1	नई सीवेज ट्रीटमेंट संयंत्र पैकेज, आरसीएफ ट्राम्बे	10/2014	197.79	197.79	37.66	11/2016	11/2016
स्वास्थ्य और परिवार कल्याण							
1	एलजीबीआरआईएमएच	07/2012	175.57	175.57	89.92	12/2014	03/2016
2	एलएचएमसी-अस्पताल	02/2013	414.11	414.11	208.71	11/2013	11/2014
3	सफदरजंग एसएसबी	09/2013	444.70	444.70	228.19	12/2015	12/2015
4	रायबरेली-हाउसिंग	10/2013	159.50	159.50	92.88	11/2013	09/2015

5	ईबी-सफदरजंग	11/2013	196.70	196.70	0.00	01/2016	01/2016
भारी उद्योग							
1	राष्ट्रीय औटोमोटिव टेस्टिंग तथा आरडी अवसंरचना परियोजना (एनएटीआरआईपी)	04/2011	1718.00	3827.30	0.00	09/2011	12/2017
खान							
1	मलंजखंड खान का विस्तार-भूमिगत खान का विकास	09/2011	1856.00	1856.00	0.00	09/2017	09/2017
पेट्रोलियम							
1	मंगलौर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	732.00	1227.00	1016.37	10/2011	03/2016
2	पादुर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	993.00	1693.00	1438.30	01/2012	03/2016
3	एन्नोर में नई विपणन टर्मिनल	11/2006	171.83	171.83	0.00	एन.ए.	एन.ए.
4	12 ऑफशोर सप्लाई वेजेल्स (ओएसवी) का निर्माण	06/2007	736.65	736.65	498.95	09/2011	06/2016
5	सं. बीस फीडर गैस पाइपलाइन	03/2009	228.64	214.19	135.00	12/2016	12/2016
विद्युत							
1	सुबनसिरी लोअर एच.ई.पी (8x250 मेवा.) (एनएचपीसी)	09/2003	6285.33	18063.89	7870.78	09/2010	एन.ए.
2	बीटीपीएस-ए	08/2006	2313.00	4237.67	3088.00	12/2011	03/2016
3	आरटीपीएस चरण-I	04/2007	4122.00	9606.82	1353.36	02/2011	01/2017
4	नॉर्थ ईआर में फाइबर ऑप्टिक संचार प्रणाली का स्थापना	03/2012	198.63	198.63	90.74	09/2014	06/2016
5	यूआरटीडीएसएम फेज-I	01/2014	374.63	374.63	5.36	04/2016	11/2016
रेलवे							
1	हावड़ा-आमता-चंपादंगा एनएल (एसईआर)	04/1974	393.46	1026.00	181.48	03/2007	03/2015
2	नांगलडैम-तलवारा (एनएल), एनआर	03/1981	450.00	2100.00	391.95	07/2012	एन.ए.
3	एकलाखी-बलूरघाट सहित जी से नई बीजी रेलवे लाइन	04/1983	36.80	1336.57	255.55	एन.ए.	03/2019
4	तामलुक दीघा, लाइन दोहरीकरण (एसईआर)	03/1984	293.97	1428.00	466.36	06/2005	12/2019
5	गुना-इटावा वाया शिवपुर-ग्वालियर-भिंड एनएल, (एनसीआर)	04/1986	158.77	608.02	602.10	03/1994	03/2015
सड़क परिवहन एवं राजमार्ग							

1	लखनऊ-रायबरेली	07/1999	635.90	635.90	0.00	07/2012	एन.ए.
2	आगरा-बाईपास (एनएस-1/उ.प्र.-1), किमी. 176.8-13.03 एनएच-2,3	07/1999	635.90	635.90	0.00	07/2012	एन.ए.
3	बिजनी से असम/प.बं.सीमा (एनएच-31.सी)(2))एनएचएआई	12/2003	348.16	348.16	269.40	09/2007	एन.ए.
4	बिजनी से असम/प.बं.सीमा (एनएच-31.सी)(1))एनएचएआई	12/2003	237.80	237.80	0.00	06/2008	एन.ए.
5	बिजनी से असम/प.बं.सीमा फेज-II किमी. 30.00 से 0.00, एनएच-31 सी	12/2003	195.00	195.00	0.00	06/2008	एन.ए.
पोत परिवहन एवं पत्तन							
1	एन्नौर मनाली एक्सप्रेस वे, एफ/ओ स्पेशल पर्पस व्हीकल	10/2002	150.00	600.00	139.80	03/2006	12/2015
2	सेतुसमुंद्रम शिप चैनल प्रोजेक्ट	06/2005	2427.40	2427.40	837.90	10/2008	एन.ए.
3	मुंबई में ऑफशोर कंटेनर बर्थ का निर्माण तथा बीओटी आधार पर कंटेनर टर्मिनल का विकास	01/2007	366.39	669.46	412.00	12/2010	01/2016
4	कोचीन पोर्ट ट्रस्ट के वल्लारपदम में आईसीटीटी के लिए रेल संपर्क	03/2007	245.67	409.83	353.18	04/2009	08/2016
5	2 ऑफशोर कंटेनर बर्थ और टर्मिनल का निर्माण और विकास	11/2007	1228.00	1460.00	1038.00	12/2010	09/2017
इस्पात							
1	सिंटर मशीनों - 1 और 2 की सुधार	12/2009	343.00	488.40	33.61	10/2016	10/2016
2	गुआ अयस्क खान	02/2014	4749.00	4749.00	1.29	09/2017	09/2017
3	गैस नेटवर्क बीएसएल	03/2015	255.19	255.19	22.05	03/2018	03/2018
4	बीएसएल में नए सिंटर प्लांट	03/2015	1034.01	1034.01	0.00	10/2017	10/2017
5	आरएसपी में नई एचएसएम	04/2015	3127.30	3127.30	156.76	04/2018	04/2018
दूरसंचार							
1	टर्नकी आधार पर बीएसएनएल में ईआरपी कार्यान्वयन	10/2009	384.00	384.00	74.74	10/2010	11/2015
2	एनएफएस	03/2012	13334.00	13334.00	0.00	07/2015	एन.ए.
शहरी विकास							
1	मिलिटरी एम में मैरेड	08/2005	191.24	191.24	0.00	08/2007	एन.ए.

	अकोमोडेशन का निर्माण						
2	आरएस के अंतर्गत बिहार राज्य में राज्य राजमार्गों का विकास	11/2006	2727.89	2727.89	0.00	03/2010	एन.ए.
3	सीवरेज परियोजना	08/2007	246.90	246.90	0.00	एन.ए.	एन.ए.
4	आईआईएसईआर कोलकाता के लिए हरिघंटा कल्याणी प.बं. में शैक्षिक सहित आवासीय परिसर	01/2009	225.81	225.81	136.53	06/2012	12/2015
5	संसदीय सौध भवन परिसर में भवन के विस्तार हेतु निर्माण कार्य	05/2009	261.85	261.85	150.77	05/2013	06/2016

एन.ए.: सूचित नहीं

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार उपलब्धियों को अंतिम रूप देने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

9. यह भी पाया गया है कि परियोजना एजेंसियां संशोधित लागत अनुमानों तथा अनेक परियोजनाओं को शुरू करने की समय-सारणी को सूचित नहीं कर रही हैं, जो संकेत देता है कि समय/लागत वृद्धि संबंधी आंकड़े कम बताए गए हैं । बिना संशोधित लागत अनुमानों वाली शुरुआती (सबसे पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई है:-

संशोधित लागत अनुमानों के बिना पहले की (सबसे पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची (30-11-2015 की स्थिति के अनुसार)

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (करोड़ रु. में)	संशोधित लागत(करोड़ रु. में)	संचयी व्यय (करोड़ रु. में)
	परमाणु ऊर्जा				
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	13171.00	17270.00	20962.00
	नागर विमानन				
1	पाकयांग (सिक्किम) हवाई अड्डा में नया हवाई अड्डा का निर्माण	01/2009	309.46	0.00	404.81
	पेट्रोरसायन				
1	असम गैस क्रेकर परियोजना	04/2006	5460.61	8920.00	9025.14

पेट्रोलियम					
1	पारादीप में विपणन टर्मिनल	07/2009	199.75	0.00	205.75
2	कोरबा में विपणन टीओपी	01/2011	141.86	0.00	159.09
3	एनबीपी क्षेत्र (डी-1) के एनबीपी-14 ब्लॉक में लोअर पेज के लिए विकास योजना	10/2013	429.06	429.00	439.02
विद्युत					
1	पार्वती एचईपी (4X200 मेगावाट) (एनएचपीसी) II	09/2002	3919.59	0.00	5328.26
2	सुबनसिरी लोअर एच.ई.पी. (8X250 मेगावाट) (एनएचपीसी)	09/2003	6285.33	0.00	7870.78
3	तीस्ता लो डैम एचईपी, चरण-IV (4X40 मेवा) (एनएचपीसी)	09/2005	1061.38	0.00	1923.42
4	किशनगंगा एचईपी (3X 110 मेवा.)	01/2009	3642.04	0.00	4276.75
5	पल्लटाना जीबीपीपी तथा बीपीटीएस से जुड़े पारेषण प्रणाली	02/2010	2144.00	0.00	2219.30
रेलवे					
1	एकलाखी-बलूरघाट सहित जी से नई बीजी रेलवे लाइन	04/1983	36.80	36.38	255.55
2	विरमगम-भिल्डी (डब्ल्यूआर), जीसी	04/1990	155.66	0.00	201.26
3	पेड़ापल्ली-करीमनगर-निजामाबाद एनएल (एससीआर)	12/1994	124.43	0.00	712.02
4	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	03/1995	2500.00	3000.00	10658.34
5	कटक-बरांग (एलडी)	04/1995	127.13	0.00	193.37
सड़क परिवहन एवं राजमार्ग					
1	धरमतुल से सोनापुर, किमी 205-183 (एएस-20)	05/2009	1108.00	0.00	3466.00
2	गुवाहाटी से नलबारी (एएस-4)	02/2009	1693.75	0.00	2762.00
3	सोनापुर से गुवाहाटी (एएस-3)	03/2010	1509.10	0.00	1675.00
4	नलबारी से बिजनी (एएस-6)	06/2010	792.06	0.00	1649.00
5	नलबारी से बिजनी (एएस-7)	04/2010	1267.00	0.00	1313.00
पोत परिवहन एवं पत्तन					
1	कोचीन पोर्ट्स के बल्लापड़म में आईसीटीटी तकरेल कनेक्टिविटी	03/2007	245.67	0.00	351.18

एन.आर.: सूचित नहीं

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार संशोधित लागत अनुमानों को अंतिम रूप देने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

10. शुरू करने की संशोधित तारीख के बिना पहले की परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची इस प्रकार है:-

शुरू करने की संशोधित अनुसूची के बिना पहले की (सबसे पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची (30.11.2015 की स्थिति के अनुसार)

क्र.सं.	परियोजना	अनुमोदन की तारीख	शुरू करने की मूल तारीख	शुरू करने की संशोधित तारीख	शुरू करने की अनुमानित तारीख
नागर विमानन					
1	10 हवाई अड्डों में एयरपोर्ट संचालन नियंत्रण केन्द्रों की स्थापना	02/2010	03/2014	एन.ए.	05/2015
2	नया अंतरराष्ट्रीय टर्मिनल भवन (गोवा) का निर्माण	05/2010	05/2012	एन.ए.	03/2015
3	विभिन्न हवाई अड्डों पर 56 एनओएस एयरफील्ड फायर टैंडर की सप्लाई	10/2012	03/2015	एन.ए.	09/2015
कोयला					
1	जल्लाराम शॉफ्ट परियोजना	09/2007	03/2013	एन.ए.	एन.ए.
स्वास्थ्य और परिवार कल्याण					
1	एलएचएमसी नया दिल्ली- पुनःविकास	02/2013	11/2013	एन.ए.	11/2014
2	एम्स रायबरेली-हाउसिंग	10/2013	11/2013	एन.ए.	09/2015
पेट्रोलियम					
1	एन्नोर में नई विपणन टर्मिनल	11/2006	एन.ए.	एन.ए.	एन.ए.
2	कोच्ची-कूटनाड बंगलोर मंगलोर पाइपलाइन परियोजना	06/2009	12/2012	एन.ए.	06/2015
3	एक ईटीपी तथा तीन ईटीपी सह वाटर इंजेक्शन प्लांट (डब्ल्यूआईपी) का निर्माण	06/2010	01/2014	एन.ए.	एन.ए.
4	एन्नोर-त्रिची-मदुरै एलपीजी पाइपलाइन	05/2013	एन.ए.	एन.ए.	एन.ए.

5	पारादीप-हल्दिया-दुर्गापुर एलपीजी पाइपलाइन का संवर्धन तथा पटना से मुजफ्फरपुर तक इसका विस्तार	01/2015	एन.ए.	एन.ए.	एन.ए.
विद्युत					
1	सुबनसिरी लोअर एच.ई.पी. (8X250 मेगावाट) (एनएचपीसी)	09/2003	09/2010	एन.ए.	एन.ए.
2	एसआरका प्रणालीसुदृढीकरण-XII	02/2010	06/2012	एन.ए.	एन.ए.
3	आंध्र प्रदेश भाग-ए1 के वैमागिरी क्षेत्र में आईएसजीएस परियोजनाओं से जुड़ी साझा प्रणाली	03/2012	06/2014	एन.ए.	एन.ए.
रेलवे					
1	हावड़ा-आमता-चंपादंगा एनएल (एसईआर)	04/1974	03/2007	03/2007	03/2015
2	नांगलडैम-तलवाड़ा (एनएल), एन.आर.	03/1981	07/2012	एन.ए.	एन.ए.
3	गुना-इटावा वाया शिवपुरी-ग्वालियर-भिंड एनएल, (एनसीआर)	04/1986	03/1994	एन.ए.	03/2015
4	नामखाना चंद्रनगर काकद्वीप-बुदाखाली तथा चंद्रनगर के लिए लक्ष्मीकांतपुर-नामखाना के बाद एमएम	04/1987	एन.ए.	एन.ए.	एन.ए.
5	विरमगम-भिल्डी (डब्ल्यूआर), जीसी	04/1990	एन.ए.	03/2010	एन.ए.
सड़क परिवहन एवं राजमार्ग					
1	लखनऊ-रायबरेली	07/1999	07/2012	एन.ए.	एन.ए.
2	बिजनी से असम यूपी/प.बं.सीमा फेज-II, किमी.30.00 से 0.00 किमी, एनएच-31सी	12/2003	06/2005	एन.ए.	एन.ए.
3	सिलचर-उदारबंद (फेज-II) एनएच-54 309 किमी से 275 किमी	12/2003	09/2007	एन.ए.	एन.ए.
4	आगरा-बाईपास (एनएस-1/यूपी-1), एनएच-2,3	12/2003	09/2007	एन.ए.	एन.ए.
5	हरंगाजो से मेबंग (एएस-23), 164.08 किमी से 190.587 किमी एनएच-54	12/2003	09/2007	एन.ए.	एन.ए.
पोत परिवहन एवं पत्तन					
1	सेतु समुद्रम शिप चैनल परियोजना	06/2005	10/2008	एन.ए.	एन.ए.
2	चीन के जियांगसू रॉगसैंग हैवी इंडस्ट्रीज कारपोरेशन लि. से वीएलसीसी के सं. दो (2) 317000 डीडब्ल्यूटी का अधिग्रहण	10/2010	11/2013	एन.ए.	11/2013
इस्पात					
1	7.0 एमटीपीए कुमारस्वामी आयरन ओर माइन प्रोजेक्ट (एनएमडीसी)	02/2011	05/2013	01/2015	08/2015

2	1.2 एमटीपीए पिल्लेट प्लांट प्रोजेक्ट, डोनिमलाई(एनएमडीसी)	04/2011	04/2013	09/2014	06/2015
3	रोघट डिपोजिट में 21 लोकेशन पर स्थायी बैरक का विकास	04/2014	04/2015	एन.ए.	एन.ए.
दूरसंचार					
1	स्पेक्ट्रम के लिए नेटवर्क	03/2012	07/2015	एन.ए.	एन.ए.
शहरी विकास					
1	सैन्य रक्षा मंत्रालय स्टेशन मामुन पंजाब में वैवाहिक आवासीय का निर्माण	08/2005	08/2007	एन.ए.	एन.ए.
2	बंगलोर मेट्रो रेल परियोजना	05/2006	06/2011	एन.ए.	एन.ए.
3	आरएसवीवाई पटना के अंतर्गत बिहार राज्य में राज्य राजमार्गों का विकास	11/2006	03/2010	एन.ए.	एन.ए.
4	मूसी के दक्षिण में पुराने शहर क्षेत्र में सेवरेज सिस्टम की पुनर्स्थापना और इसका सुदृढीकरण (2 जोन में)	08/2007	एन.ए.	एन.ए.	एन.ए.
5	आईआईटी हौजखास नई दिल्ली में लेक्चर थिएटर और लैब कम्प्लेक्स	01/2010	07/2012	एन.ए.	एन.ए.

एन.ए.: सूचित नहीं

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार कार्य शुरू करने की संशोधित समय-सारणी को अंतिम रूप देने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

11. अतिरिक्त विलंब का क्षेत्र-वार ब्योरा निम्नानुसार है:-

i) **कोयला क्षेत्र में,** 81 परियोजनाओं में से 43 परियोजनाएं विलंबित हैं । माह के दौरान केवल 1 परियोजना "विंड पावर परियोजना, काझूनेरकुलम, तमिलनाडु, एनएलसी" ने निजी भूमि अधिग्रहण और उपकरणों की आपूर्ति तथा सिविल कार्यों में विलंब के कारण 4 माह का अतिरिक्त विलंब होने की सूचना दी है ।

ii) **पेट्रोलियम क्षेत्र में,** 63 परियोजनाओं में से 37 परियोजनाएं विलंबित हैं । माह के दौरान, 10 परियोजनाओं के संबंध में 1-6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । 10 परियोजनाओं में से 3 मेगा परियोजनाएं हैं; 'सीपीसीएल स्थित माउंडिड बुलेट परियोजना' और 'गुजरात रिफाइनरी, आईओसीएल में ईटीपी के लिए रिवर्स ऑसमोसिस प्लांट' ने क्रमशः एचटी ट्रांसमिशन में अड़चन और एनएएसटी के कॉन्ट्रैक्टर द्वारा धीमी प्रगति के कारण 1 माह के अतिरिक्त विलंब की सूचना दी है । 'पारादीप रिफाइनरी परियोजना, आईओसीएल' और 'अपग्रेडेशन ऑफ कूड ऑयल पंप स्टेशन ऑफ

नाहरकटिया-बरौनी कूड ऑयल ट्रंक पाइपलाईन ऑयल' ने क्रमशः स्टीम टर्बाइन जेनरेटर-1 की मरम्मत और मुख्य लाइन पंप के वितरण में विलंब के कारण 2 माह के विलंब की सूचना दी है। परियोजना '6 ईटीपी का निर्माण, ओएनजीसी' और 'कोरबा में मार्किटिंग टॉप, आईओसीएल' में प्रत्येक ने क्रमशः इंजीनियरिंग और खरीद सेवाओं में विलंब तथा ठेकेदारों के खराब प्रदर्शन के कारण 3 माह के विलंब की सूचना दी है। परियोजना 'कन्वर्सन ऑफ रिज सागर सम्राट टू मोबाइल ऑफशोर प्रोडक्शन यूनिट (एमओपीएस), ओएनजीसी' और 'पारादीप हल्दिया दुर्गापुर एलपीजी पाइपलाईन, आईओसीएल' ने क्रमशः ठेकेदार द्वारा इस्पात की खरीद और द्वितीय चरण वन स्वीकृति में विलंब के कारण क्रमशः 4 माह और 6 माह के विलंब की सूचना दी है। परियोजना 'पारादीप, आईओसीएल में मार्किटिंग टर्मिनल' और ऊरन चाकन/शिकरपुर एलपीजी पाइपलाईन ने क्रमशः 1 माह और 5 माह के विलंब की सूचना दी है (तथापि, इन परियोजनाओं में विलंब के मामले में परियोजना क्रियान्वयन एजेंसियों द्वारा कोई विशिष्ट कारण सूचित नहीं किए गए हैं)।

iii) **विद्युत क्षेत्र में**, 105 परियोजनाओं में से, 57 परियोजनाएं विलंबित हैं। माह के दौरान 18 परियोजनाओं के संबंध में 1-16 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 18 परियोजनाओं में से 15 परियोजनाएं मेगा परियोजनाएं हैं। इनमें से 4 परियोजनाओं में गंभीर आरओयू समस्या के कारण प्रत्येक में 1 माह का विलंब है तथा 1 परियोजना भूमि अधिग्रहण में विलंब के कारण 1 माह से विलंबित है। 2 परियोजनाएं आरओयू समस्याओं के कारण 2 माह से विलंबित हैं और 4 परियोजनाएं क्रमशः संविदा मुद्दे पहुंच मार्ग में कटाव के कारण बांधों तक पहुंच में बाधा, भूमि अधिग्रहण में देरी और जेनरेटर स्टार्टर की आपूर्ति में विलंब के कारण विलंबित हैं। परियोजना 'बीबीसीएल-नबीनगर टीपीपी-जेबवी (4x250 मेगावाट) एनटीपीसी' भूमि अधिग्रहण में विलंब के कारण 3 माह से विलंबित है। परियोजना 'कामेंग जल विद्युत परियोजना नीपको' और 'कॉमन एसवाईएस एसोसिएटेड विद ईस्ट कोस्ट एनर्जी प्रा. लि. एंड एनसीसी पावर परियोजना लि. एलटीओए जनरल पार्ट-बी, पीजीसीआईएल' ने प्रत्येक ने क्रमशः कानून और व्यवस्था की समस्या और गंभीर आरओयू समस्या के कारण 6 माह के विलंब की सूचना दी है। परियोजना 'नार्थ-ईस्ट नॉर्थ वेस्ट्रन इंटरकनेक्टर परियोजना, पीजीसीआईएल और टूरियल जल विद्युत परियोजना, नीपको ने क्रमशः कानून और व्यवस्था की समस्या और सामग्री के परिवहन को प्रभावित करने वाली खराब सड़क परिस्थितियों की वजह से प्रत्येक ने 1 माह के विलंब की सूचना दी है। परियोजना टिहरी पंप भंडारण संयंत्र (1000 मेगावाट), टीएचडीसीएल ने भू विचलन से संबंधित न्यायालय मामलों की वजह से 1 माह के विलंब की सूचना दी है। (तथापि, इन परियोजनाओं में विलंब के मामले में परियोजना क्रियान्वयन एजेंसियों द्वारा कोई विशिष्ट कारण सूचित नहीं किए गए हैं)।

iv) **इस्पात क्षेत्र में**, 22 परियोजनाओं में से 10 परियोजनाएं विलंबित हैं। माह के दौरान 3 परियोजनाओं 'आरएसपी, सेल स्थित कोक ओवन बैटरी-3 का पुनर्निर्माण; बीएसपी, सेल स्थित कोक ओवन बैटरी-9 की कोल्ड रिपेयर; और 'भिलाई इस्पात संयंत्र, सेल का विस्तार' ने क्रमशः 1 माह, 2 माह

और 3 माह के अतिरिक्त विलंब की सूचना दी है (तथापि, इन परियोजनाओं में विलंब के मामले में परियोजना क्रियान्वयन एजेंसियों द्वारा कोई विशिष्ट कारण सूचित नहीं किए गए हैं) ।

v) **शहरी विकास क्षेत्र में**, 12 परियोजनाएं विलंबित हैं । माह के दौरान, 1 परियोजना 'आईआईएम, सीपीडब्ल्यूडी के लिए स्थाई परिसर के चरणबद्ध निर्माण का चरण-I' ने 4 माह के अतिरिक्त विलंब की सूचना दी है (तथापि, इन परियोजनाओं में विलंब के मामले में परियोजना क्रियान्वयन एजेंसियों द्वारा कोई विशिष्ट कारण सूचित नहीं किए गए हैं) ।

vi) **सड़क परिवहन एवं राजमार्ग क्षेत्र में**, 163 परियोजनाओं में से, 9 परियोजनाएं विलंबित हैं । माह के दौरान, 1 परियोजना 'सोनापुर से गुवाहाटी (एस-3), एनएचआई' ने 3 माह के अतिरिक्त विलंब की सूचना दी है (तथापि, इन परियोजनाओं में विलंब के मामले में परियोजना क्रियान्वयन एजेंसियों द्वारा कोई विशिष्ट कारण सूचित नहीं किए गए हैं) ।

vii) **परमाणु ऊर्जा क्षेत्र में**, सभी 4 परियोजनाएं विलंबित हैं । माह के दौरान, 1 परियोजना 'राजस्थान परमाणु विद्युत परियोजना-7 और 8 (2X700 मेगावाट) एनपीसीआईएल ने विभिन्न विक्रेताओं से उपकरणों की आपूर्ति में विलंब की वजह से 1 माह के अतिरिक्त विलंब की सूचना दी है ।

12. रेल मंत्रालय ने इस मंत्रालय को रेलवे द्वारा कार्यान्वित की जा रही सभी जारी परियोजनाओं पर मासिक स्थिति रिपोर्टें प्रस्तुत करने की परंपरा को समाप्त कर दिया है । अतः उपलब्ध सूचना/आंकड़े (जनवरी 2015 की स्थिति के अनुसार) रेलवे क्षेत्र की सभी परियोजनाओं के संबंध में उपयोग किए गए ।

13. एनएचआई जून 2015 से सभी चालू सड़क क्षेत्र परियोजनाओं की पूर्ण सूचना नियमित रूप से उपलब्ध नहीं करा रही है । नवंबर, 2015 के दौरान 137 परियोजनाओं में से केवल 37 परियोजनाओं के आंकड़े/सूचना एनएचआई द्वारा ऑनलाइन उपलब्ध कराई गई थी । शेष परियोजनाओं के संबंध में आंकड़े/सूचना एनएचआई द्वारा सूचित पिछले आंकड़ों के अनुसार है ।

14. दिनांक 30.11.2015 की स्थिति के अनुसार, विभिन्न क्षेत्रों में ₹ 150 करोड़ तथा अधिकलागत वाली परियोजनाओं के संबंध में स्थिति रिपोर्ट में सूचित की गई है ।

15. इसे सचिव, सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय का अनुमोदन प्राप्त है ।

EXECUTIVE SUMMARY

1. The Flash Report for November 2015 contains information on the status of the 787 Central Sector Infrastructure Projects costing ₹150 crore and above. During November 2015, only 1 project in Power sector has reported completion.

2. During the reference month, out of 787 projects, 208 projects are delayed with respect to original schedule and 35 projects have reported additional delay vis-à-vis the date of completion reported in the previous month. Of these 35 projects, 20 are Mega Projects costing ₹ 1000 crore and above.

S.No.	Sector	Projects on monitor (No.)	Delayed Projects w.r.t original schedule (No.)	Additionally delayed during the month under report (No.)	Additionally delayed Mega Projects (No.)
1	RAILWAYS	296	27	0	0
2	ROAD TRANSPORT AND HIGHWAYS	163	9	1	0
3	POWER	105	57	18	15
4	COAL	81	43	1	0
5	PETROLEUM	63	37	10	3
6	URBAN DEVELOPMENT	31	12	1	0
7	STEEL	22	10	3	1
8	CIVIL AVIATION	5	1	0	0
9	SHIPPING AND PORTS	6	4	0	0
10	HEALTH AND FAMILY WELFARE	5	1	0	0
11	ATOMIC ENERGY	4	4	1	1
12	TELECOMMUNICATIONS	2	1	0	0
13	FERTILISERS	1	0	0	0
14	MINES	1	0	0	0
15	PETROCHEMICALS	1	1	0	0
16	HEAVY INDUSTRIES	1	1	0	0
Total		787	208	35	20

3. Total original cost of implementation of the 787 projects was ₹10,20,904.25 crore and their anticipated completion cost is likely to be ₹12,32,092.39 crore, which reflects overall cost overruns of ₹2,11,188.14 crore (20.69% of original cost). The expenditure incurred on these projects till November 2015 is ₹ 4,85,200.10 crore, which is 39.38% of the anticipated cost of the projects. The

sector-wise list of projects (maximum five in numbers) having maximum percentage of cost overruns
is as follows:-

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Percentage of Cost
Overruns (as on 30-11-2015)**

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (%)
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	13171.00	22462.00	70.54
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	5677.00	62.57
CIVIL AVIATION					
1	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	217.60	244.10	12.18
COAL					
1	ADRIYALA SHAFT PROJECT	12/2009	212.34	1228.39	478.50
2	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	10/2007	259.40	486.57	87.58
3	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	11/2009	150.59	198.59	31.87
4	RFR OF MANUGURU OC PROJECT	11/2012	430.45	486.27	12.97
5	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	479.53	479.63	0.02
HEAVY INDUSTRY					
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	1718.00	3827.30	122.78
PETROCHEMICALS					
1	ASSAM GAS CRACKER PROJECT	04/2006	5460.61	9965.00	82.49
PETROLEUM					
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	70.49
2	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	01/2006	732.00	1227.00	67.62
3	MARKETING TOP AT KORBA	01/2011	141.86	232.00	63.54
4	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	12/2009	309.81	462.79	49.38
5	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	1256.72	45.83
POWER					
1	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	07/1998	368.72	1381.71	274.73
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	18063.89	187.40
3	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	6476.34	159.38
4	PARE HYDRO ELECTRIC PROJECT	12/2008	573.99	1487.49	159.15
5	TRIPURA GAS BASED POWER PROJECT	07/2009	421.01	1007.57	139.32
RAILWAYS					
1	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	36.80	1336.57	3531.98
2	BANKURA - DAMODAR (GC) (SER)	03/1998	111.90	2371.85	2019.62
3	AKOLA-KHANDWA GC AKOLA-AKOT	04/2008	184.26	2000.00	985.42
4	BANGLORE - SATYAMANGALAM (NL)(SWR)	04/1996	138.00	1382.78	902.01
5	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	09/1995	100.00	980.00	880.00
ROAD TRANSPORT AND HIGHWAYS					
1	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	106.50
2	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	385.13	92.75
3	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	155.04	280.13	80.68
4	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	331.23	68.99
5	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S	03/2011	218.31	339.82	55.66

SHIPPING AND PORTS					
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	300.00
2	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	82.72
3	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	245.67	409.83	66.82
4	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL	11/2007	1228.00	1460.00	18.89
STEEL					
1	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	42.39
URBAN DEVELOPMENT					
1	BANGALORE METRO RAIL PROJECT	05/2006	6395.00	11609.00	81.53

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

4. The sector wise list of projects (maximum five in numbers) having maximum cost overruns (COR) in absolute term is as below:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Cost Overruns (COR)

(as on 30-11-2015)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (Rs.crore)
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	13171.00	22462.00	9291.00
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	5677.00	2185.00
CIVIL AVIATION					
1	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	217.60	244.10	26.50
COAL					
1	ADRIYALA SHAFT PROJECT	12/2009	212.34	1228.39	1016.05
2	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	10/2007	259.40	486.57	227.17
3	RFR OF MANUGURU OC PROJECT	11/2012	430.45	486.27	55.82
4	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	11/2009	150.59	198.59	48.00
5	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	479.53	479.63	0.10
HEAVY INDUSTRY					
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	1718.00	3827.30	2109.30
PETROCHEMICALS					
1	ASSAM GAS CRACKER PROJECT	04/2006	5460.61	9965.00	4504.39
PETROLEUM					
1	PARADIP REFINERY PROJECT	02/2009	29777.00	34555.00	4778.00
2	INTEGRATED REFINERY EXPANSION PROJECT	03/2012	14225.00	16504.00	2279.00
3	INTEGRATED DEVELOPMENT OF BASSEIN FIELD	12/2012	3513.07	4619.94	1106.87
4	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	05/2013	4124.35	4941.49	817.14
5	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	700.00
POWER					

1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	18063.89	11778.56
2	BARH STPP(3X660MW) NTPC	02/2005	8692.97	15095.67	6402.70
3	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	04/2007	4122.00	9606.82	5484.82
4	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	6476.34	3979.44
5	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	7818.68	3899.09
RAILWAYS					
1	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	19565.00	17065.00
2	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	727.56	6570.75	5843.19
3	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	04/1996	1676.31	5500.00	3823.69
4	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	09/1997	1500.00	4996.19	3496.19
5	SEVOK RANGPO, NEFR	04/2008	1339.48	4190.00	2850.52
ROAD TRANSPORT AND HIGHWAYS					
1	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	1180.00
2	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	385.13	185.32
3	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	331.23	135.23
4	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	155.04	280.13	125.09
5	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S	03/2011	218.31	339.82	121.51
SHIPPING AND PORTS					
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	450.00
2	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	303.07
3	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL	11/2007	1228.00	1460.00	232.00
4	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	245.67	409.83	164.16
STEEL					
1	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	145.40
URBAN DEVELOPMENT					
1	BANGALORE METRO RAIL PROJECT	05/2006	6395.00	11609.00	5214.00

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

5. Out of the 787 projects, 7 projects are ahead of schedule, 146 are on schedule and 208 are delayed with respect to their original schedule. However, the number of delayed projects decreases to 174 if delay is calculated on the basis of latest schedule of completion. Further, 30 projects have been sanctioned without original commissioning schedule date and for 396 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 208 delayed projects, 35

projects have overall delay in the range of 1 to 12 months, 49 projects have delay in the range of 13 to 24 months, 73 projects have delay in the range of 25 to 60 months and 51 projects have delay of 61 months and above. The sector wise list of projects (maximum five in numbers) having maximum time overruns (TOR) are as below:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Time Overruns (TOR)
(as on 30-11-2015)

SN	PROJECT	DOA	DOC ORIGINAL	DOC ANTICIPATED	TOR(IN MONTHS)
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	12/2008	06/2016	90
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	09/2010	09/2016	72
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	10/2017	22
4	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016	05/2018	17
CIVIL AVIATION					
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	01/2011	09/2017	80
COAL					
1	MAGADH OC 20 MTY (CCL)	08/2008	07/2012	03/2021	104
2	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	03/2010	03/2017	84
3	KULDA OCP (MAHANADI COALFIELDS LTD)	01/2005	03/2010	03/2016	72
4	ASHOK EXPN OCP CCL (10 MTY)	12/2007	03/2011	03/2017	72
5	JHANJRA R-VI SEAM PSLW	11/2006	03/2011	03/2017	72
HEALTH AND FAMILY WELFARE					
1	LGBRIMH-TEZPUR, ASSAM	07/2012	12/2014	03/2016	15
HEAVY INDUSTRY					
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	04/2011	09/2011	12/2017	75
PETROCHEMICALS					
1	ASSAM GAS CRACKER PROJECT	04/2006	04/2012	12/2015	44
PETROLEUM					
1	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I	07/2009	01/2013	12/2018	71
2	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH)	12/2009	06/2011	03/2016	57
3	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	06/2007	09/2011	06/2016	57
4	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	01/2006	10/2011	03/2016	53
5	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	01/2012	03/2016	50
POWER					
1	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	07/1998	07/2006	10/2017	135
2	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	09/2009	12/2018	111
3	BARH STPP(3X660MW) NTPC	02/2005	01/2011	05/2018	88

4	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009	12/2016	84
5	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	09/2005	09/2009	06/2016	81
RAILWAYS					
1	GONDIA-JABALPUR(GC),(SECR)	02/1997	03/1998	12/2019	261
2	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	11/2002	12/2018	193
3	BANKURA - DAMODAR (GC) (SER)	03/1998	03/2005	12/2019	177
4	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	06/2005	12/2019	174
5	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	03/1996	03/2004	03/2016	144
ROAD TRANSPORT AND HIGHWAYS					
1	NALBARI T BIJNI (AS-7)	12/2003	04/2008	01/2017	105
2	SONAPUR TO GUWAHTI (AS-3)	12/2003	03/2008	04/2016	97
3	NALBARI TO BIJNI (AS-6)	12/2003	06/2008	04/2016	94
4	GUWAHTI TO NALBARI (AS-4)	12/2003	04/2008	12/2015	92
5	GUWAHATI TO NALBARI (AS-5)	12/2003	04/2008	12/2015	92
SHIPPING AND PORTS					
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	03/2006	12/2015	117
2	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	04/2009	08/2016	88
3	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL	11/2007	12/2010	09/2017	81
4	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	12/2010	01/2016	61
STEEL					
1	EXPANSION OF BHILAI STEEL PLANT	08/2010	03/2013	06/2016	39
2	INSTALLATION OF 45 MVA SAF T WITH OTHER ASSOCIATED FACILITIES	12/2011	10/2013	03/2016	29
3	SMS-1 CONVERTERS REVAMPING	05/2012	07/2015	03/2017	20
4	NMDC INTEGRATED STEEL PLANT	01/2010	05/2015	12/2016	19
5	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH	07/2012	08/2014	01/2016	17
TELECOMMUNICATIONS					
1	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS	10/2009	10/2010	11/2015	61
URBAN DEVELOPMENT					
1	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA	01/2009	06/2012	12/2015	42
2	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI	05/2009	05/2013	06/2016	37

3	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL	12/2012	12/2014	12/2016	24
4	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	07/2012	08/2014	01/2016	17
5	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	11/2012	11/2014	03/2016	16

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further time overruns.

6. In April 2015, out of 758 projects on the monitor of this Ministry, 231 projects reported cost overruns and 323 projects reported time overruns; while during November 2015, out of 787 projects, 228 projects reported cost overruns and 208 projects reported time overruns. In comparison to April 2015, number of **projects** reporting **cost overruns** has gone **down** from **30.47%** to **28.97%** whereas **projects** reporting **time overruns** have **decreased** from **42.61%** to **26.43%**.

7. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in forest clearance, delay in supply of equipments, fund constraints, geological surprises, problems in equipment erection, geo-mining conditions, slow progress in civil works, shortage of labour, inadequate mobilization by the contractor, maoist problems, court cases, contractual issues, ROU/ROW problems, law and order situation etc.

8. The Online Computerized Monitoring System (OCMS) of this Ministry envisages monitoring of milestones of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The sector wise list of earliest projects (maximum five in numbers) without milestones are as below:-

**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Milestones
(as on 30-11-2015)**

S N	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST ANTICIPATED (Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)	ORIGINAL DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
CIVIL AVIATION							
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG (SIKKIM) AIR	01/2009	309.46	309.46	404.81	01/2011	09/2017
2	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AI	02/2010	344.28	344.28	80.60	03/2014	05/2015

3	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING	05/2010	335.61	318.00	305.01	05/2012	03/2015
4	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	217.60	244.10	30.66	03/2015	09/2015
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRP	10/2013	314.61	314.61	18.02	N.A.	09/2018
COAL							
1	DURGAPUR OCP	02/2015	916.24	916.24	0.00	03/2023	03/2023
2	AMGAON OC RCE	07/2015	316.10	316.10	15.85	03/2020	03/2020
3	BATURA H/W PROJECT	07/2015	231.92	231.92	0.00	03/2022	03/2022
FERTILISERS							
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	197.79	37.66	11/2016	11/2016
HEALTH AND FAMILY WELFARE							
1	LGBRIMH	07/2012	175.57	175.57	89.92	12/2014	03/2016
2	LHMC - HOSPITAL	02/2013	414.11	414.11	208.71	11/2013	11/2014
3	SAFDARJUNG SSB	09/2013	444.70	444.70	228.19	12/2015	12/2015
4	RAEBARELI-HOUSING	10/2013	159.50	159.50	92.88	11/2013	09/2015
5	EB-SAFDARJUNG	11/2013	196.70	196.70	0.00	01/2016	01/2016
HEAVY INDUSTRY							
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT	04/2011	1718.00	3827.30	0.00	09/2011	12/2017
MINES							
1	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MIN	09/2011	1856.00	1856.00	0.00	09/2017	09/2017
PETROLEUM							
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	01/2006	732.00	1227.00	1016.37	10/2011	03/2016
2	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	1438.30	01/2012	03/2016
3	NEW MARKETING	11/2006	171.83	171.83	0.00	N.A.	N.A.

	TERMINAL AT ENNORE						
4	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	06/2007	736.65	736.65	498.95	09/2011	06/2016
5	TWENTY NOS. FEEDER GAS LINES	03/2009	228.64	214.19	135.00	12/2016	12/2016
POWER							
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	18063.89	7870.78	09/2010	N.A.
2	BTPS-A	08/2006	2313.00	4237.67	3088.00	12/2011	03/2016
3	RTPS PH-I	04/2007	4122.00	9606.82	1353.36	02/2011	01/2017
4	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER	03/2012	198.63	198.63	90.74	09/2014	06/2016
5	URTDSM PHASE-I	01/2014	374.63	374.63	5.36	04/2016	11/2016
RAILWAYS							
1	HOWRAH-AMTA-CHAMPADANG A NL (SER)	04/1974	393.46	1026.00	181.48	03/2007	03/2015
2	NANGALDAM-TALWARA(NL),N R	03/1981	450.00	2100.00	391.95	07/2012	N.A.
3	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING G	04/1983	36.80	1336.57	255.55	N.A.	03/2019
4	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	293.97	1428.00	466.36	06/2005	12/2019
5	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR)	04/1986	158.77	608.02	602.10	03/1994	03/2015
ROAD TRANSPORT AND HIGHWAYS							
1	LUCKNOW-RAIBAREILI	07/1999	635.90	635.90	0.00	07/2012	N.A.
2	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3	12/2003	348.16	348.16	269.40	09/2007	N.A.
3	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI)	12/2003	237.80	237.80	0.00	06/2008	N.A.
4	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	12/2003	195.00	195.00	0.00	06/2008	N.A.
5	BIJNI TO ASSAM/WB BORDER PH.II,	12/2003	230.00	230.00	0.00	06/2005	N.A.

	KM.30.00 TO 0.00, NH-31 C						
SHIPPING AND PORTS							
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI	10/2002	150.00	600.00	139.80	03/2006	12/2015
2	SETHUSAMUDR AM SHIP CHANNEL PROJECT	06/2005	2427.40	2427.40	837.90	10/2008	N.A.
3	CONSTRUCTIO N OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF	01/2007	366.39	669.46	412.00	12/2010	01/2016
4	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS	03/2007	245.67	409.83	353.18	04/2009	08/2016
5	CONSTRUCTIO N AND DEVELOPMENT OF 2 OFFSHORE CONTAIN	11/2007	1228.00	1460.00	1038.00	12/2010	09/2017
STEEL							
1	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	33.61	10/2016	10/2016
2	GUA ORE MINES	02/2014	4749.00	4749.00	1.29	09/2017	09/2017
	GAS NETWORK BSL	03/2015	255.19	255.19	22.05	03/2018	03/2018
3	NEW SINTER PLANT AT BSL	03/2015	1034.01	1034.01	0.00	10/2017	10/2017
4	NEW HSM AT RSP	04/2015	3127.30	3127.30	156.76	04/2018	04/2018
TELECOMMUNICATIONS							
1	ERP IMPLEMENTATI ON IN BSNL ON TURNKEY BASIS	10/2009	384.00	384.00	74.74	10/2010	11/2015
2	NFS	03/2012	13334.0 0	13334.00	0.00	07/2015	N.A.
URBAN DEVELOPMENT							
1	CONSTRUCTIO N OF MARRIED ACCOMODATIO N AT MILITARY M	08/2005	191.24	191.24	0.00	08/2007	N.A.
2	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RS	11/2006	2727.89	2727.89	0.00	03/2010	N.A.
3	SEWEWRAGE	08/2007	246.90	246.90	0.00	N.A.	N.A.

	PROJECT						
4	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA	01/2009	225.81	225.81	136.53	06/2012	12/2015
5	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEX	05/2009	261.85	261.85	150.77	05/2013	06/2016

N.A.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up milestones.

9. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The sector wise list of earliest (oldest) projects (maximum five in numbers) without revised cost estimates are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Cost Estimates (as on 30-11-2015)

SN	PROJECT	DOA	COST ORIGINAL (Rs. Crore)	COST REVISED (Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	13171.00	17270.00	20962.00
CIVIL AVIATION					
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	309.46	0.00	404.81
PETROCHEMICALS					
1	ASSAM GAS CRACKER PROJECT	04/2006	5460.61	8920.00	9025.14
PETROLEUM					
1	MARKETING TERMINAL AT PARADEEP	07/2009	199.75	0.00	205.75
2	MARKETING TOP AT KORBA	01/2011	141.86	0.00	159.09
3	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1)	10/2013	429.06	429.00	439.02
POWER					
1	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	0.00	5328.26
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	0.00	7870.78
3	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	09/2005	1061.38	0.00	1923.42
4	KISHANGANGA HEP (3X110 MW)	01/2009	3642.04	0.00	4276.75
5	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	02/2010	2144.00	0.00	2219.30
RAILWAYS					
1	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-	04/1983	36.80	36.38	255.55

	ITAHAR(NL),NEFR				
2	VIRAMGAM-BHILDI(WR),GC	04/1990	155.66	0.00	201.26
3	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	12/1994	124.43	0.00	712.02
4	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	3000.00	10658.34
5	CUTTACK - BARANG (LD)	04/1995	127.13	0.00	193.37
ROAD TRANSPORT AND HIGHWAYS					
1	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	160.00	0.00	197.60
2	GUWHAITI TO NALBARI (AS-4)	12/2003	175.96	0.00	182.50
3	SONAPUR TO GUWAHTI (AS-3)	12/2003	245.00	0.00	491.20
4	NALBARI TO BIJNI (AS-6)	12/2003	225.00	0.00	258.40
5	NALBARI T BIJNI (AS-7)	12/2003	208.00	230.00	290.60

N.R.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised cost estimates.

10. The sector wise list of earliest projects (maximum five in numbers) without revised commissioning schedule are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Commissioning Schedule (as on 30-11-2015)

SN	SECTOR/ PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	REVISED DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
CIVIL AVIATION					
1	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS	02/2010	03/2014	N.A.	05/2015
2	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING (GOA)	05/2010	05/2012	N.A.	03/2015
3	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	03/2015	N.A.	09/2015
COAL					
1	JALLARAM SHAFT PROJECT	09/2007	03/2013	N.A.	N.A.
HEALTH AND FAMILY WELFARE					
1	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	11/2013	N.A.	11/2014
2	AIIMS-RAEBARELI-HOUSING	10/2013	11/2013	N.A.	09/2015
PETROLEUM					
1	NEW MARKETING TERMINAL AT ENNORE	11/2006	N.A.	N.A.	N.A.
2	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT	06/2009	12/2012	N.A.	06/2015

3	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	06/2010	01/2014	N.A.	N.A.
4	ENNORE-TRICHY-MADURAI LPG PIPELINE	05/2013	N.A.	N.A.	N.A.
5	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	01/2015	N.A.	N.A.	N.A.
POWER					
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	09/2010	N.A.	N.A.
2	SYSTEM STRENGTHENING XII OF SR	02/2010	06/2012	N.A.	N.A.
3	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1	03/2012	06/2014	N.A.	N.A.
RAILWAYS					
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	03/2007	03/2007	03/2015
2	NANGALDAM-TALWARA(NL),NR	03/1981	07/2012	N.A.	N.A.
3	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	04/1986	03/1994	N.A.	03/2015
4	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	04/1987	N.A.	N.A.	N.A.
5	VIRAMGAM-BHILDI(WR),GC	04/1990	N.A.	03/2010	N.A.
ROAD TRANSPORT AND HIGHWAYS					
1	LUCKNOW-RAIBAREILI	07/1999	07/2012	N.A.	N.A.
2	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C	12/2003	06/2005	N.A.	N.A.
3	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	12/2003	09/2007	N.A.	N.A.
4	AGRA-BYPASS(NS-1/UP-1), NH-2,3	12/2003	09/2007	N.A.	N.A.
5	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54	12/2003	09/2007	N.A.	N.A.
SHIPPING AND PORTS					
1	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	10/2008	N.A.	N.A.

2	ACQUISITION OF TWO (2) NOS OF 317000 DWT VLCC'S FROM JIANGSU RONGSHENG HEAVY INDUSTRIES CO.LTD.,CHIN	10/2010	11/2013	N.A.	11/2013
	STEEL				
1	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC)	02/2011	05/2013	01/2015	08/2015
2	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC)	04/2011	04/2013	09/2014	06/2015
3	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT	04/2014	04/2015	N.A.	N.A.
	TELECOMMUNICATIONS				
1	NETWORK FOR SPECTRUM	03/2012	07/2015	N.A.	N.A.
	URBAN DEVELOPMENT				
1	CONSTRUCTION OF MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB	08/2005	08/2007	N.A.	N.A.
2	BANGALORE METRO RAIL PROJECT	05/2006	06/2011	N.A.	N.A.
3	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA	11/2006	03/2010	N.A.	N.A.
4	REHABILITATION AND STRENGTHENING OF SEWETRAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI(IN ZONE 2 IN	08/2007	N.A.	N.A.	N.A.
5	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI	01/2010	07/2012	N.A.	N.A.

N.A.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised commissioning schedule.

11. The Sector-wise details of additional delays are as under:-

- i) In the **Coal Sector**, out of 81 projects, 43 projects are delayed. During the month, only 1 project 'Wind Power project, Kazhuneerkulam, Tamilnadu, NLC' has reported additional delay of 4 months due to delay in acquisition of private land, delay in supply of equipments and civil works.
- ii) In the **Petroleum Sector**, out of 63 projects, 37 projects are delayed. During the month,

10 projects have reported additional delays in the range of 1-6 months. Out of 10 projects, 3 projects are mega projects. The projects 'Mounded Bullet Project at CPCL' and 'Reverse Osmosis Plant for ETP at Gujarat Refinery, IOCL', have reported additional delay of 1 month each due to hindrances in HT transmission and slow progress by LSTK contractor respectively. 'Paradip Refinery Project, IOCL' and 'Upgradation of Crude Oil Pump Stations of Naharkatiya- Barauni Crude Oil Trunk Pipeline Oil' have reported delay of 2 months each due to repair of steam turbine generator – I and delay in delivery of mainline pumps respectively. The projects 'Constructions of 6 ETPs, ONGC' and 'Marketing Top at Korba, IOCL' have reported delay of 3 months each due to delay in engineering & procurement services and poor performance of Contractors respectively. The projects 'Conversion of Rig Sagar Samrat to Mobile Offshore Production Unit (MOPS), ONGC' and 'Paradip Haldia Durgapur LPG Pipeline, IOCL' have reported delay of 4 months and 6 months respectively due to delay in procurement of Steel by the contractors and delay in 2nd stage forest clearance respectively. The Projects 'Marketing Terminal at Paradeep, IOCL' and 'Uran Chakan/Shikrapur LPG Pipeline, HPCL' have reported delay of 1 month and 5 months respectively (however, no specific reasons have been reported by the project implementing agencies for the delay in these projects).

- iii) In the **Power Sector**, out of 105 projects, 57 projects are delayed. During the month, 18 projects have reported additional delay in the range of 1-16 months. Out of 18 projects, 15 are mega projects. Of these 4 projects are delayed by 1 month each due to severe ROU problems and 1 project is delayed by 1 month due to delay in land acquisition. 2 projects are delayed by 2 months due to ROU problems and 4 projects are delayed by 2 months each due to contractual issue, access to restriction to dam site due to erosion of approach road, delay in land acquisition and delay in supply of generator stator respectively. The project 'BBCL-Nabinagar TPP- JV (4x250MW), NTPC' is delayed by 3 months due to delay in land acquisition. The project 'Kameng Hydroelectric Project NEEPCO' and 'Common SYS. Associated with East Coast Energy Pvt Ltd and NCC Power Projects Ltd LTOA Gen Part – B, PGCIL' have reported delay of 6 months each due to law & order problem and severe ROU problems respectively. The projects 'North-East North Western Interconnector Project, PGCIL' and 'Tural Hydro Electric Project (60MW), NEEPCO' have reported delay of 12 months each due to law & order problem and bad road condition affecting transportation of materials respectively. The project 'Tehri Pumped Storage Plant (1000MW), THDCL' has reported delay of 16 months due to court cases relating to land diversion. The project 'Tripura Gas Based Project, NEEPCO' has reported delay of 1 month (however, no specific reasons have been reported by the project implementing agencies for the delay in this project).

- iv) In the **Steel Sector**, out of 22 projects, 10 projects are delayed. During the month, 3 projects 'Rebuilding of Coke Oven Battery – 3 at RSP, SAIL', 'Cold Repair of Coke Oven Battery – 9 at BSP, SAIL' and 'Expansion of Bhilai Steel Plant, SAIL' have reported additional delay of 1 month, 2 months and 3 months respectively (however, no specific reasons have been reported by the project implementing agencies for the delay in these projects).
- v) In the **Urban Development Sector**, out of 31 projects, 12 projects are delayed. During the month, 1 project 'Stage – I of Phase Construction of Permanent Campus for IIM, CPWD', has reported additional delay of 4 months (however, no specific reason has been reported by the project implementing agency for the delay in project).
- vi) In the **Road Transport & Highways Sector**, out of 163 projects, 9 projects are delayed. During the month, 1 project 'Sonapur to Guwahati (AS – 3), NHAI', has reported additional delay of 3 months (however, no specific reason has been reported by the project implementing agency for the delay in project).
- vii) In the **Atomic Energy sector**, all 4 projects are delayed. During the month 1 project 'Rajasthan Atomic Power Project-7 and 8 (2x700MW), NPCIL', has reported additional delay of 1 month due to delay in supply of equipments from various vendors.

12. Ministry of Railway has **discontinued** the practice of furnishing monthly status reports on all on-going projects being implemented by Railways to this Ministry. Therefore, the available information/data (**as on January 2015**) has been used in respect of all projects of Railways sector.

13. NHAI is not regularly furnishing the complete information of all on-going Road sector projects since June 2015. During November 2015, out of 137 projects, the data/information of only 37 projects were furnished online by NHAI. The data/information in respect of remaining projects is as per last reported data by NHAI.


14. The status as on 30.11.2015 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

15. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

EXECUTIVE SUMMARY

Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	296	0
2	ROAD TRANSPORT AND HIGHWAYS	163	1
3	POWER	105	18
4	COAL	81	1
5	PETROLEUM	63	10
6	URBAN DEVELOPMENT	31	1
7	STEEL	22	3
8	SHIPPING AND PORTS	6	0
9	CIVIL AVIATION	5	0
10	HEALTH AND FAMILY WELFARE	5	0
11	ATOMIC ENERGY	4	1
12	TELECOMMUNICATIONS	2	0
13	FERTILISERS	1	0
14	MINES	1	0
15	PETROCHEMICALS	1	0
16	HEAVY INDUSTRY	1	0
	Total	787	35

Sectoral break up of on-going infrastructure projects.

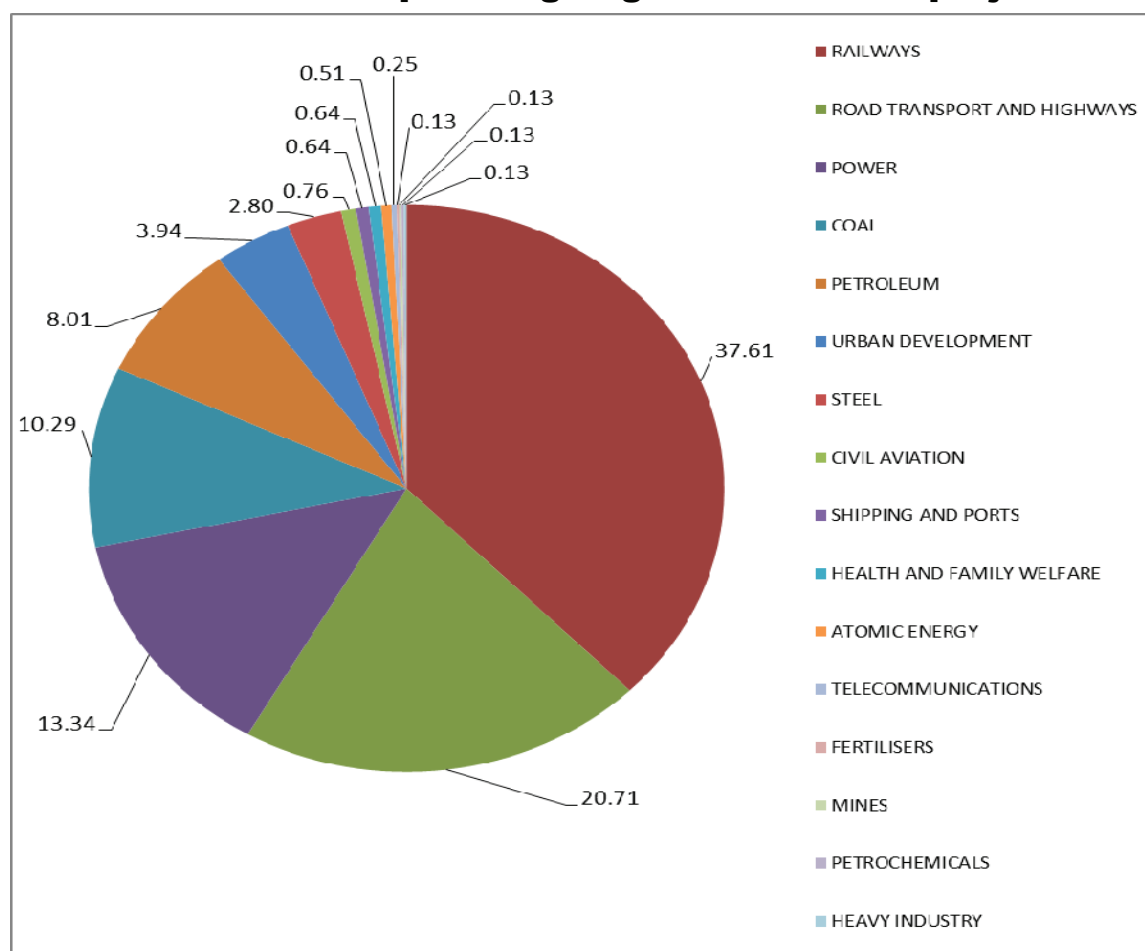

**Month wise List of Completed Projects Costing Rs.150 crore and above during
2015-2016**

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2015			
	<u>PETROLEUM</u>			
1	KOTA JOBNER PIPELINE PROJECT (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000170]	276.26	12/2015	241.63
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
2	PUNE-SHOLAPUR,PKG1 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000127]	1,110.00	05/2012	1,802.00
	May,2015			
	<u>PETROLEUM</u>			
3	DEVELOPMENT OF B-193 CLUSTER FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000033]	3,248.78	08/2010	5,933.42
4	DEVELOPMENT OF CLUSTER-7 FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000104]	4,550.40	03/2013	2,583.55
5	PIPELINE REPLACEMENT PROJECT-3 (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000137]	2,547.26	05/2014	1,412.08
	<u>POWER</u>			
6	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000127]	901.77	08/2014	945.20
7	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000136]	803.34	03/2015	593.19
	<u>TELECOMMUNICATIONS</u>			
8	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G (BHARAT SANCHAR NIGAM LIMITED) - [N26000062]	336.81	01/2009	199.37
	June,2015			
	<u>STEEL</u>			
9	EXPANSION OF DURGAPUR STEEL PLANT (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000074]	2,875.00	12/2012	2,640.00
10	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000075]	254.55	11/2013	135.89
	<u>POWER</u>			
11	KOLDAM HEP (NTPC) (NATIONAL THERMAL POWER CORPORATION) - [180100211]	4,527.15	04/2009	6,622.00

Month wise List of Completed Projects Costing Rs.150 crore and above during 2015-2016				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
12	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000105]	1,366.34	12/2013	1,320.96
	<u>RAILWAYS</u>			
13	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) (NORTH EASTERN RAILWAY) - [220100255]	863.23	-	888.87
14	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR (NORTH EAST FRONTIER RAILWAY) - [220100315]	915.70	-	3,198.30
	July,2015			
	<u>STEEL</u>			
15	AUGMENTATION OF IRON ORE STORAGE IN RMHP (RASTRIYA ISPAT NIGAM LIMITED) - [N12000053]	480.00	09/2009	388.52
	<u>PETROLEUM</u>			
16	SURAT PARADIP PIPELINE PROJECT (GAS AUTHORITY OF INDIA LIMITED) - [N16000163]	10,281.00	04/2015	1.49
	<u>POWER</u>			
17	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000130]	1,263.26	11/2014	1,131.58
	August,2015			
	<u>CIVIL AVIATION</u>			
18	GAGAN PROJECT (AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000065]	626.00	06/2013	483.53
	<u>COAL</u>			
19	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) (NEYVELI LIGNITE CORPORATION) - [060100087]	2,030.78	06/2009	3,215.91
20	TUTICORIN THERMAL POWER PROJECT- 2X500 MW (NEYVELI LIGNITE CORPORATION) - [N06000047]	4,904.54	03/2012	6,426.43
	<u>PETROLEUM</u>			
21	DEVELOPMENT OF G1 AND GS-15 (ONGCL) (OIL & NATURAL GAS CORPORATION LIMITED) - [160100231]	429.82	04/2006	3,439.38
22	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000098]	288.04	08/2012	229.16
23	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000123]	331.20	08/2013	190.04
24	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG (INDIAN STRATEGIC PETROLEUM RESERVES LTD) - [N16000156]	672.00	10/2011	1,082.12

**Month wise List of Completed Projects Costing Rs.150 crore and above during
2015-2016**

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	<u>POWER</u>			
25	BARH STPP STAGE -II (NATIONAL THERMAL POWER CORPORATION) - [N18000047]	7,341.04	10/2013	8,962.00
26	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000076]	4,672.99	11/2012	3,769.57
27	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000096]	2,569.25	03/2014	2,876.57
28	VINDHYACHAL STPP STAGE-V (NATIONAL THERMAL POWER CORPORATION) - [N18000134]	3,180.40	08/2015	2,042.00
	September,2015			
	<u>STEEL</u>			
29	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) (NATIONAL MINERAL DEVELOPMENT CORPORATION (NMDC)) - [N12000018]	607.17	12/2011	394.89
30	EXPANSION OF BOKARO STEEL PLANT (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000055]	6,325.00	12/2011	5,256.65
	<u>PETROLEUM</u>			
31	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000132]	5,608.40	05/2015	4,457.47
	<u>POWER</u>			
32	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000124]	213.78	03/2014	204.54
33	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000154]	1,315.90	10/2016	632.97
34	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) (NORTH EAST ELECTRIC POWER CORPORATION) - [N18000156]	296.87	12/2014	318.66
	October,2015			
	<u>CIVIL AVIATION</u>			
35	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II (AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000070]	452.00	03/2015	449.41
	<u>STEEL</u>			
36	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) (RASTRIYA ISPAT NIGAM LIMITED) - [120100067]	8,692.00	10/2009	11,483.12
37	CAPTIVE POWER PLANT - 2 (RASTRIYA ISPAT NIGAM LIMITED) - [N12000087]	677.00	09/2013	537.19

Month wise List of Completed Projects Costing Rs.150 crore and above during 2015-2016				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	<u>PETROLEUM</u>			
38	102 MW WIND POWER PROJECT (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000119]	1,106.00	06/2012	437.69
	<u>POWER</u>			
39	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) (POWER GRID CORPORATION OF INDIA LIMITED) - [180100246]	588.25	12/2007	1,020.81
40	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000093]	2,743.19	12/2013	2,827.00
	<u>URBAN DEVELOPMENT</u>			
41	FARIDABAD EXTENSION (DELHI METRO RAIL CORPORATION LTD) - [N28000057]	2,494.00	09/2014	1,311.53
	November, 2015			
	<u>POWER</u>			
42	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID (POWER GRID CORPORATION OF INDIA LIMITED) - [N16000144]	1,508.74	03/2015	1,211.48

**Month wise List of Deleted Projects Costing Rs.150 crore and above during
2015-2016**

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	May,2015			
	<u>PETROLEUM</u>			
1	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000170]	723.64	03/2013	.00
2	AHMEDABAD REDEVELOPMENT PROJECT (OIL & NATURAL GAS CORPORATION LIMITED) - [N24000127]	1,916.10	12/2014	1,160.14
3	MEHESANA REDEVELOPMENT PROJECT (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000033]	3,823.00	04/2015	1,076.57
4	ANKLESWAR REDEVELOPMENT (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000104]	2,189.63	12/2014	1,034.30
5	INTEGRATED DEVELOPMENT OF BASSEIN FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000137]	3,513.07	02/2016	.47
6	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS (OIL & NATURAL GAS CORPORATION LIMITED) - [N18000127]	2,913.10	05/2016	13.86
	June,2015			
7	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS (OIL & NATURAL GAS CORPORATION LIMITED) - [N18000136]	2,913.10	05/2016	13.86
8	IMPROVED OIL RECOVERY OF B-173A FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N26000062]	352.49	03/2014	122.87
	<u>TELECOMMUNICATIONS</u>			
9	EXECUTION OF TELECOM NETWORK REQUIREMENT OF DEFENCE FORCES (BHARAT SANCHAR NIGAM LIMITED) - [N12000074]	1,077.00	03/2009	.00
	August,2015			
	<u>SHIPPING AND PORTS</u>			
10	MODIFICATION AND STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 (PORT TRUST) - [N12000075]	277.00	03/2012	.21
11	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS(PORT TRUST) - [180100211]	830.00	05/2013	.00
	October,2015			
	<u>PETROLEUM</u>			
12	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS (OIL & NATURAL GAS CORPORATION LIMITED) - [N18000105]	2,913.10	05/2016	13.86
13	IMPROVED OIL RECOVERY OF B-173A FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [220100255]	352.49	03/2014	.00

Month wise List of Deleted Projects Costing Rs.150 crore and above during 2015-2016				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	<u>SHIPPING AND PORTS</u>			
14	MODIFICATION AND STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 (PORT TRUST) - [220100315]	277.00	03/2012	.21
15	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS(PORT TRUST) - [N12000053]	830.00	05/2013	.00


Summary of projects in the Flash Report for the month of November, 2015

Project Implementation - Current Status:

Number of Projects in Previous Month	782
Number of Projects completed/dropped/frozen in Current Month	1
Number of Projects elevated to the status of Major project during the current month	2
Number of Projects Added in Current Month	4
Number of Projects in Current Month	787


Brief Analysis

Project Status with respect to Original Schedule: Out of 787 projects, 7 projects are ahead of schedule, 146 projects are on schedule 208 projects are delayed. 396 projects do not have fixed dates of commissioning. 30 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

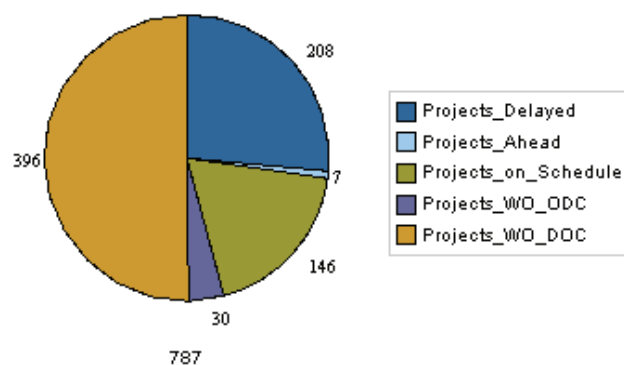

Investment Scenario

Total original cost of implementation of 787 projects when sanctioned, was of the order of Rs. 1020904.25 crore but this was subsequently revised to Rs. 1232092.39 crore implying a cost overrun of 20.7%. The expenditure incurred on these projects till November, 2015 is Rs. 485200.1 crore, which is 39.4% of the revised cost of the projects.

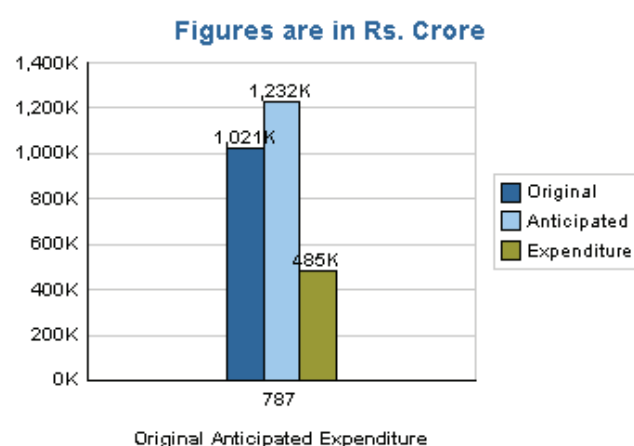

Projects Added / Completed / Dropped / Frozen

No of Projects in Previous Month	782
No of Projects Completed/Dropped/Frozen in Current Month	1
No of Projects added in Current Month	4
No of Projects elevated to the status of Major Project during current month	2
No of Projects in Current Month	787

Project status

Number of Projects							
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total	Delayed Projects (%)
Original (Date)	208	7	146	30	396	787	26.43
Latest Approved (Date)	174	9	178	30	396	787	22.11

Project cost

(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	671	8,26,035.96	9,16,429.63	3,00,286.26	32.80	90,393.67	10.90
Project with Revision in Cost	116	2,54,468.37	3,15,662.76	1,84,913.84	58.60	61,194.39	24.00
Total	787	10,80,504.33	12,32,092.39	4,85,200.10	39.38	151588.06	14.03
Original Cost of All Projects							
Original Cost	787	10,20,904.25	12,32,092.39	4,85,200.10	39.38	2,11,188.14	20.69

Delayed Project cost

(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	208	455,789.45	576,028.57	332,124.65	57.70	120,239.12	26.40
Latest Approved (RCE)	174	418,315.66	484,803.44	291,196.63	60.10	66,487.78	15.90

Additional Delayed Project cost						
(All Cost/ Expenditure in Rs. crore)						
Cost overrun						
No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
35	124,777.94	147,658.56	111,773.14	75.70	22,880.62	18.30

Extent of cost overrun in projects with respect to original schedule(Sector Wise)									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun ^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost Overrun^ (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	2	16,663.00	28,139.00	68.87
2	CIVIL AVIATION	5	1,521.56	1,530.45	0.58	1	217.60	244.10	12.18
3	COAL	81	56,886.73	57,765.87	1.55	5	1,532.31	2,879.45	87.92
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0.00
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	0.00
6	STEEL	22	49,833.99	49,979.39	0.29	1	343.00	488.40	42.39
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	1	5,460.61	9,965.00	82.49
8	PETROLEUM	63	133,205.31	144,838.01	8.73	18	68,022.56	80,741.01	18.70
9	POWER	105	294,151.17	341,570.36	16.12	21	60,901.26	108,384.06	77.97
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
11	HEALTH AND FAMILY WELFARE	5	1,390.58	1,390.58	0.00	0	0.00	0.00	0.00
12	RAILWAYS *	296	171,881.41	296,947.84	72.76	160	81,685.74	208,168.14	154.84
13	ROAD TRANSPORT AND HIGHWAYS **	163	106,445.00	108,621.05	2.04	13	3,920.93	6,121.59	56.13
14	SHIPPING AND PORTS	6	5,412.28	5,968.93	10.28	4	1,990.06	3,139.29	57.75
15	TELECOMMUNICATIONS	2	13,718.00	13,718.00	0.00	0	0.00	0.00	0.00
16	URBAN DEVELOPMENT	31	136,783.82	141,997.82	3.81	1	6,395.00	11,609.00	81.53
Total		787	1,020,904.25	1,232,092.39	20.69	228	248,850.07	463,706.34	86.34

* - Information in respect of Ministry of Railways is as on 01.01.2015. Ministry of Railways is not updating the information.

** - Out of 137 projects, the data / information of only 37 projects were submitted online by the NHAI for the month of November 2015. The data / information in respect of remaining projects is as per last reported data i.e. June 2015.

^ - Cost Overrun = Anticipated Cost minus Original Cost.

<u>Extent of cost overrun in projects with respect to original schedule(State Wise)</u>									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun ^			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost Overrun ^ (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	31	16,552.09	18,701.39	12.99	6	2,006.14	4,155.44	107.14
2	ARUNACHAL PRADESH	3	9,356.22	26,027.72	178.19	3	9,356.22	26,027.72	178.19
3	ASSAM	35	22,431.10	38,134.44	70.01	14	15,918.17	31,722.22	99.28
4	BIHAR	48	50,822.31	64,600.51	27.11	15	13,737.73	28,243.47	105.59
5	GOA	5	1,395.15	1,377.54	-1.26	0	0.00	0.00	0.00
6	GUJARAT	25	28,672.83	29,670.47	3.48	5	2,873.48	3,998.44	39.15
7	HARYANA	9	4,659.81	6,630.43	42.29	3	1,633.56	3,604.18	120.63
8	HIMACHAL PRADESH	4	7,154.09	12,973.29	81.34	2	4,966.47	10,785.67	117.17
9	JAMMU AND KASHMIR	7	21,314.62	40,235.30	88.77	2	6,142.04	25,062.72	308.05
10	KARNATAKA	33	65,975.04	80,937.81	22.68	17	13,700.79	28,669.59	109.26
11	KERALA	15	24,980.58	29,455.73	17.91	8	17,335.36	21,810.51	25.82
12	MADHYA PRADESH	19	22,774.88	24,985.97	9.71	5	2,404.35	5,034.88	109.41
13	MAHARASHTRA	55	104,291.59	114,584.52	9.87	13	21,963.17	33,300.60	51.62
14	MANIPUR	1	727.56	6,570.75	803.12	1	727.56	6,570.75	803.12
15	MEGHALAYA	3	4,845.02	6,069.90	25.28	1	4,083.02	5,307.90	30.00
16	MIZORAM	2	988.06	4,201.96	325.27	2	988.06	4,201.96	325.27
17	NAGALAND	2	5,124.00	7,461.12	45.61	2	5,124.00	7,461.12	45.61
18	ODISHA	41	69,443.31	78,531.35	13.09	15	35,919.03	45,028.41	25.36
19	PUNJAB	4	1,180.50	1,153.46	-2.29	0	0.00	0.00	0.00
20	RAJASTHAN	31	27,361.24	27,844.69	1.77	6	2,574.16	3,142.63	22.08
21	SIKKIM	2	1,648.94	4,499.46	172.87	1	1,339.48	4,190.00	212.81
22	TAMIL NADU	41	61,482.24	81,074.93	31.87	18	23,092.91	42,685.60	84.84
23	TRIPURA	4	2,381.35	6,012.47	152.48	4	2,381.35	6,012.47	152.48
24	UTTAR PRADESH	30	36,002.28	38,782.69	7.72	7	1,739.99	4,568.66	162.57
25	WEST BENGAL	39	44,085.90	58,961.63	33.74	13	8,617.64	24,016.70	178.69
26	D & N HAVELI	1	6,086.08	6,086.08	0.00	0	0.00	0.00	0.00
27	DELHI	14	49,464.96	49,464.96	0.00	0	0.00	0.00	0.00
28	CHHATISGARH	29	81,307.10	82,969.27	2.04	6	3,494.57	5,157.04	47.57
29	JHARKHAND	38	39,714.33	42,197.08	6.25	6	3,485.18	6,009.67	72.44
30	UTTARAKHAND	6	9,351.89	11,651.71	24.59	3	4,855.31	7,155.13	47.37
31	ANDAMAN & NICOBAR ISLANDS	1	314.61	314.61	0.00	0	0.00	0.00	0.00
32	TELANGANA	31	11,908.91	14,872.86	24.89	8	2,417.24	5,381.19	122.62
33	MULTI STATE	178	187,105.66	215,056.29	14.94	42	35,973.09	64,401.67	79.03
Total		787	1,020,904.25	1,232,092.39	20.69	228	248,850.07	463,706.34	86.34

^ - Cost Overrun = Anticipated Cost minus Original Cost.

Extent of time overrun in projects with respect to original schedule									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns \$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost Overrun ^ (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	4	40,442.00	51,918.00	17 - 90
2	CIVIL AVIATION	5	1,521.56	1,530.45	0.58	1	309.46	309.46	80 - 80
3	COAL	81	56,886.73	57,765.87	1.55	43	24,482.34	25,466.46	8 - 104
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	-
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	-
6	STEEL	22	49,833.99	49,979.39	0.29	10	36,011.40	36,011.40	4 - 39
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	1	5,460.61	9,965.00	44 - 44
8	PETROLEUM	63	133,205.31	144,838.01	8.73	37	80,641.12	89,203.56	1 - 71
9	POWER	105	294,151.17	341,570.36	16.12	57	153,605.70	189,246.33	2 - 135
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
11	HEALTH AND FAMILY WELFARE	5	1,390.58	1,390.58	0.00	1	175.57	175.57	15 - 15
12	RAILWAYS *	296	171,881.41	296,947.84	72.76	27	29,410.10	85,131.16	3 - 261
13	ROAD TRANSPORT AND HIGHWAYS **	163	106,445.00	108,621.05	2.04	9	1,940.27	2,032.22	24 - 105
14	SHIPPING AND PORTS	6	5,412.28	5,968.93	10.28	4	1,990.06	3,139.29	61 - 117
15	TELECOMMUNICATIONS	2	13,718.00	13,718.00	0.00	1	384.00	384.00	61 - 61
16	URBAN DEVELOPMENT	31	136,783.82	141,997.82	3.81	12	79,218.82	79,218.82	2 - 42
Total		787	1,020,904.25	1,232,092.39	20.69	208	455,789.45	576,028.57	

* - Information in respect of Ministry of Railways is as on 01.01.2015. Ministry of Railways is not updating the information.

** - Out of 137 projects, the data / information of only 37 projects were submitted online by the NHAI for the month of November 2015. The data / information in respect of remaining projects is as per last reported data i.e. June 2015.

\$ - Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus Original Cost.

<u>Extent of time overrun in projects with respect to original schedule(State Wise)</u>									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns \$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost Overrun ^ (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	31	16,552.09	18,701.39	12.99	4	1,792.43	1,792.43	11 - 24
2	ARUNACHAL PRADESH	3	9,356.22	26,027.72	178.19	2	3,070.89	7,963.83	33 - 84
3	ASSAM	35	22,431.10	38,134.44	70.01	15	18,181.97	32,817.91	15 - 110
4	BIHAR	48	50,822.31	64,600.51	27.11	6	19,627.45	29,560.97	5 - 98
5	GOA	5	1,395.15	1,377.54	-1.26	0	0.00	0.00	-
6	GUJARAT	25	28,672.83	29,670.47	3.48	4	12,489.08	12,412.39	1 - 42
7	HARYANA	9	4,659.81	6,630.43	42.29	0	0.00	0.00	-
8	HIMACHAL PRADESH	4	7,154.09	12,973.29	81.34	2	4,190.42	8,089.51	16 - 111
9	JAMMU AND KASHMIR	7	21,314.62	40,235.30	88.77	2	6,142.04	25,062.72	10 - 193
10	KARNATAKA	33	65,975.04	80,937.81	22.68	3	16,564.19	17,231.27	2 - 53
11	KERALA	15	24,980.58	29,455.73	17.91	2	1,238.67	2,102.83	50 - 88
12	MADHYA PRADESH	19	22,774.88	24,985.97	9.71	4	1,881.51	2,010.54	12 - 69
13	MAHARASHTRA	55	104,291.59	114,584.52	9.87	16	54,468.29	60,875.96	7 - 144
14	MANIPUR	1	727.56	6,570.75	803.12	1	727.56	6,570.75	96 - 96
15	MEGHALAYA	3	4,845.02	6,069.90	25.28	0	0.00	0.00	-
16	MIZORAM	2	988.06	4,201.96	325.27	2	988.06	4,201.96	47 - 135
17	NAGALAND	2	5,124.00	7,461.12	45.61	1	850.00	2,973.42	60 - 60
18	ODISHA	41	69,443.31	78,531.35	13.09	14	35,771.20	40,942.89	4 - 84
19	PUNJAB	4	1,180.50	1,153.46	-2.29	0	0.00	0.00	-
20	RAJASTHAN	31	27,361.24	27,844.69	1.77	1	12,320.00	12,320.00	17 - 17
21	SIKKIM	2	1,648.94	4,499.46	172.87	2	1,648.94	4,499.46	51 - 80
22	TAMIL NADU	41	61,482.24	81,074.93	31.87	11	45,126.36	57,432.14	4 - 117
23	TRIPURA	4	2,381.35	6,012.47	152.48	3	2,129.35	5,125.82	29 - 108
24	UTTAR PRADESH	30	36,002.28	38,782.69	7.72	5	11,232.29	12,527.55	9 - 84
25	WEST BENGAL	39	44,085.90	58,961.63	33.74	12	21,324.73	31,071.30	3 - 177
26	D & N HAVELI	1	6,086.08	6,086.08	0.00	1	6,086.08	6,086.08	10 - 10
27	DELHI	14	49,464.96	49,464.96	0.00	4	40,136.16	40,136.16	9 - 37
28	CHHATISGARH	29	81,307.10	82,969.27	2.04	15	55,943.90	56,425.96	12 - 72
29	JHARKHAND	38	39,714.33	42,197.08	6.25	18	8,051.36	10,390.52	2 - 138
30	UTTARAKHAND	6	9,351.89	11,651.71	24.59	3	7,127.06	9,316.74	43 - 78
31	ANDAMAN & NICOBAR ISLANDS	1	314.61	314.61	0.00	0	0.00	0.00	-
32	TELANGANA	31	11,908.91	14,872.86	24.89	11	3,359.39	4,375.44	8 - 72
33	MULTI STATE	178	187,105.66	215,056.29	14.94	44	63,320.07	71,712.02	1 - 261
Total		787	1,020,904.25	1,232,092.39	20.69	208	455,789.45	576,028.57	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus Original Cost.

<u>Extent of time overrun in projects with respect to latest schedule</u>									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns \$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost Overrun ^ (%)	No.	Original cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	4	40,442.00	51,918.00	17 - 90
2	CIVIL AVIATION	5	1,521.56	1,530.45	0.58	1	309.46	309.46	80 - 80
3	COAL	81	56,886.73	57,765.87	1.55	40	17,085.56	17,842.51	8 - 104
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	-
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	-
6	STEEL	22	49,833.99	49,979.39	0.29	9	20,486.40	20,486.40	4 - 39
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	1	5,460.61	9,965.00	44 - 44
8	PETROLEUM	63	133,205.31	144,838.01	8.73	25	54,819.59	60,486.96	1 - 71
9	POWER	105	294,151.17	341,570.36	16.12	51	138,127.40	164,490.96	2 - 111
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
11	HEALTH AND FAMILY WELFARE	5	1,390.58	1,390.58	0.00	1	175.57	175.57	15 - 15
12	RAILWAYS *	296	171,881.41	296,947.84	72.76	24	22,935.10	72,607.16	3 - 261
13	ROAD TRANSPORT AND HIGHWAYS **	163	106,445.00	108,621.05	2.04	2	510.54	510.54	24 - 24
14	SHIPPING AND PORTS	6	5,412.28	5,968.93	10.28	4	1,990.06	3,139.29	61 - 117
15	TELECOMMUNICATIONS	2	13,718.00	13,718.00	0.00	1	384.00	384.00	61 - 61
16	URBAN DEVELOPMENT	31	136,783.82	141,997.82	3.81	10	78,660.29	78,660.29	2 - 37
Total		787	1,020,904.25	1,232,092.39	20.69	174	383,104.58	484,803.44	

* - Information in respect of Ministry of Railways is as on 01.01.2015. Ministry of Railways is not updating the information.

** - Out of 137 projects, the data / information of only 37 projects were submitted online by the NHAI for the month of November 2015. The data / information in respect of remaining projects is as per last reported data i.e. June 2015.

\$ - Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus Original Cost.

<u>Extent of cost overrun in projects with respect to latest schedule</u>									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overruns ^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun ^ (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	44,541.00	51,918.00	16.56	2	20,762.00	28,139.00	35.53
2	CIVIL AVIATION	5	1,521.56	1,530.45	0.58	1	217.60	244.10	12.18
3	COAL	81	57,718.07	57,765.87	0.08	2	630.12	678.22	7.63
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0.00
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	0.00
6	STEEL	22	49,833.99	49,979.39	0.29	1	343.00	488.40	42.39
7	PETROCHEMICALS	1	8,920.00	9,965.00	11.72	1	8,920.00	9,965.00	11.72
8	PETROLEUM	63	142,153.76	144,838.01	1.89	6	16,219.52	19,055.34	17.48
9	POWER	105	322,244.28	341,570.36	6.00	7	28,130.34	47,456.42	68.70
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
11	HEALTH AND FAMILY WELFARE	5	1,390.58	1,390.58	0.00	0	0.00	0.00	0.00
12	RAILWAYS *	296	185,296.44	296,947.84	60.26	154	87,045.00	200,328.20	130.14
13	ROAD TRANSPORT AND HIGHWAYS **	163	106,768.14	108,621.05	1.74	12	3,783.63	5,683.15	50.20
14	SHIPPING AND PORTS	6	5,842.90	5,968.93	2.16	3	1,751.22	2,469.83	41.03
15	TELECOMMUNICATIONS	2	13,718.00	13,718.00	0.00	0	0.00	0.00	0.00
16	URBAN DEVELOPMENT	31	136,783.82	141,997.82	3.81	1	6,395.00	11,609.00	81.53
Total		787	1,080,504.33	1,232,092.39	14.03	191	175,915.43	329,943.96	87.56

* - Information in respect of Ministry of Railways is as on 01.01.2015. Ministry of Railways is not updating the information.

** - Out of 137 projects, the data / information of only 37 projects were submitted online by the NHAI for the month of November 2015. The data / information in respect of remaining projects is as per last reported data i.e. June 2015.

^ - Cost Overrun = Anticipated Cost minus Original Cost.

Extent of time & cost overrun in projects with respect to latest schedule									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time \$ & cost ^ overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun ^ (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	1	13,171.00	22,462.00	90- 90
2	CIVIL AVIATION	5	1,521.56	1,530.45	0.58	0	0.00	0.00	0- 0
3	COAL	81	56,886.73	57,765.87	1.55	1	259.40	486.57	60- 60
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0- 0
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	0- 0
6	STEEL	22	49,833.99	49,979.39	0.29	0	0.00	0.00	0- 0
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	1	5,460.61	9,965.00	44- 44
8	PETROLEUM	63	133,205.31	144,838.01	8.73	7	41,311.65	49,339.67	12- 38
9	POWER	105	294,151.17	341,570.36	16.12	12	30,547.09	47,655.79	17- 135
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	0	0.00	0.00	0- 0
11	HEALTH AND FAMILY WELFARE	5	1,390.58	1,390.58	0.00	0	0.00	0.00	0- 0
12	RAILWAYS *	296	171,881.41	296,947.84	72.76	4	5,873.07	10,121.84	48- 174
13	ROAD TRANSPORT AND HIGHWAYS **	163	106,445.00	108,621.05	2.04	2	425.61	517.56	70- 105
14	SHIPPING AND PORTS	6	5,412.28	5,968.93	10.28	1	245.67	409.83	88- 88
15	TELECOMMUNICATIONS	2	13,718.00	13,718.00	0.00	0	0.00	0.00	0- 0
16	URBAN DEVELOPMENT	31	136,783.82	141,997.82	3.81	0	0.00	0.00	0- 0
	Total	787	1020904.25	1232092.39	20.69	29	97294.1	140958.26	

* - Information in respect of Ministry of Railways is as on 01.01.2015. Ministry of Railways is not updating the information.

** - Out of 137 projects, the data / information of only 37 projects were submitted online by the NHAI for the month of November 2015. The data / information in respect of remaining projects is as per last reported data i.e. June 2015.

\$ - Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus Original Cost.

Extent of time & cost overrun in projects with respect to original schedule									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time \$ & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun ^ (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	2	16,663.00	28,139.00	72- 90
2	CIVIL AVIATION	5	1,521.56	1,530.45	0.58	0	0.00	0.00	0- 0
3	COAL	81	56,886.73	57,765.87	1.55	3	951.27	2,194.59	36- 60
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0- 0
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	0- 0
6	STEEL	22	49,833.99	49,979.39	0.29	0	0.00	0.00	0- 0
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	1	5,460.61	9,965.00	44- 44
8	PETROLEUM	63	133,205.31	144,838.01	8.73	11	44,107.75	53,699.40	12- 53
9	POWER	105	294,151.17	341,570.36	16.12	18	52,349.15	87,521.64	10- 135
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75- 75
11	HEALTH AND FAMILY WELFARE	5	1,390.58	1,390.58	0.00	0	0.00	0.00	0- 0
12	RAILWAYS *	296	171,881.41	296,947.84	72.76	24	21,423.70	77,144.76	3- 261
13	ROAD TRANSPORT AND HIGHWAYS **	163	106,445.00	108,621.05	2.04	1	217.61	309.56	70- 70
14	SHIPPING AND PORTS	6	5,412.28	5,968.93	10.28	4	1,990.06	3,139.29	61- 117
15	TELECOMMUNICATIONS	2	13,718.00	13,718.00	0.00	0	0.00	0.00	0- 0
16	URBAN DEVELOPMENT	31	136,783.82	141,997.82	3.81	0	0.00	0.00	0- 0
Total		787	1020904.25	1232092.39	20.69	65	144881.15	265940.54	

* - Information in respect of Ministry of Railways is as on 01.01.2015. Ministry of Railways is not updating the information.

** - Out of 137 projects, the data / information of only 37 projects were submitted online by the NHAI for the month of November 2015. The data / information in respect of remaining projects is as per last reported data i.e. June 2015.

\$ - Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus Original Cost.

List of projects completed/dropped/Frozen during current month							(All Cost /Expenditure in Rs. crore)
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>POWER</u>						
1	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID	06/2012	1,508.74	03/2015	1,508.74	11/2015	1,211.48

List of projects added					(All Cost in Rs. crore)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
1	REHABILITATION & UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE-DORNALA T-JUNCTION) T	2/2014	258.99	7/2014	258.99	7/2016
2	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC	7/2014	251.55	2/2015	251.55	2/2017
3	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T	3/2015	175.03	/	175.03	-
	<u>URBAN DEVELOPMENT</u>					
4	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CENTRA	12/2015	209.00	/	209.00	-

Milestones (Total & achieved)

Total	3670
Achieved up to month	1740



List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>ATOMIC ENERGY</u>						
1	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) NPCIL	12,320.00	12,320.00	12/2016	04/2018	05/2018	1
	<u>COAL</u>						
2	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU NLC	364.75	364.75	10/2014	11/2015	03/2016	4
	<u>STEEL</u>						
3	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA SAIL	237.09	237.09	12/2014	12/2015	01/2016	1
4	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH SAIL	332.65	332.65	08/2014	11/2015	01/2016	2
5	EXPANSION OF BHILAI STEEL PLANT SAIL	17,265.00	17,265.00	03/2013	03/2016	06/2016	3
	<u>PETROLEUM</u>						
6	MOUNDED BULLET PROJECT AT CPCL CPCL	279.00	279.00	12/2014	11/2015	12/2015	1
7	MARKETING TERMINAL AT PARADEEP IOCL	199.75	239.73	07/2013	10/2015	11/2015	1
8	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY IOCL	160.00	160.00	02/2016	02/2016	03/2016	1
9	PARADIP REFINERY PROJECT IOCL	29,777.00	34,555.00	11/2012	11/2015	01/2016	2
10	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE OIL	871.35	1,200.00	03/2015	06/2016	08/2016	2
11	CONSTRUCTION OF 6 ETPS ONGC	317.64	240.95	09/2012	12/2015	03/2016	3
12	MARKETING TOP AT KORBA IOCL	141.86	232.00	09/2016	12/2015	03/2016	3
13	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) ONGC	861.79	1,256.72	05/2013	12/2015	04/2016	4

List of projects reporting additional delays



Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
14	URAN CHAKAN/SHIKRAPUR LPG PIPELINE HPCIL	309.81	462.79	10/2014	10/2016	03/2017	5
15	PARADIP HALDIA DURGAPUR LPG PIPELINE IOCL	913.00	913.00	08/2015	06/2016	12/2016	6
	<u>POWER</u>						
16	TRIPURA GAS BASED POWER PROJECT NEEPCO	421.01	1,007.57	07/2013	11/2015	12/2015	1
17	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME PGCIL	965.58	965.58	11/2012	12/2015	01/2016	1
18	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A PGCIL	2,074.86	2,348.37	03/2013	12/2015	01/2016	1
19	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI PGCIL	1,677.57	1,677.57	04/2013	12/2015	01/2016	1
20	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B PGCIL	1,927.16	1,927.16	10/2014	12/2015	01/2016	1
21	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII PGCIL	524.40	524.40	05/2015	12/2015	01/2016	1
22	BARH STPP(3X660MW) NTPC	8,692.97	15,095.67	01/2011	03/2018	05/2018	2
23	PARE HYDRO ELECTRIC PROJECT NEEPCO	573.99	1,487.49	08/2013	03/2016	05/2016	2
24	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B PGCIL	1,585.12	1,585.12	11/2013	01/2016	03/2016	2
25	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 PGCIL	2,422.66	2,422.66	08/2014	12/2015	02/2016	2
26	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV PGCIL	297.33	346.79	08/2014	12/2015	02/2016	2
27	KUDGI STPP STAGE 1 NTPC	15,166.19	15,166.19	01/2017	01/2017	03/2017	2
28	BRBCL-NABINAGAR TPP- JV (4X250 MW) NTPC	5,353.00	5,353.00	05/2014	06/2017	09/2017	3
29	KAMENG HYDROELECTRIC PROJECT (NEEPCO) NEEPCO	2,496.90	6,476.34	12/2009	06/2016	12/2016	6
30	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B PGCIL	2,514.88	2,514.88	12/2015	06/2016	12/2016	6
31	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT PGCIL	11,130.19	13,762.80	08/2013	12/2016	12/2017	12

List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
32	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) NEEPCO	368.72	1,381.71	07/2006	10/2016	10/2017	12
33	TEHRI PUMPED STORAGE PLANT(1000MW) THDCIL	1,657.00	2,978.86	02/2016	05/2018	09/2019	16
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
34	SONAPUR TO GUWAHTI (AS-3) NHAI	245.00	245.00	03/2008	01/2016	04/2016	3
	<u>URBAN DEVELOPMENT</u>						
35	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM CPWD	332.72	332.72	09/2016	09/2016	01/2017	4



Graphical Presentation

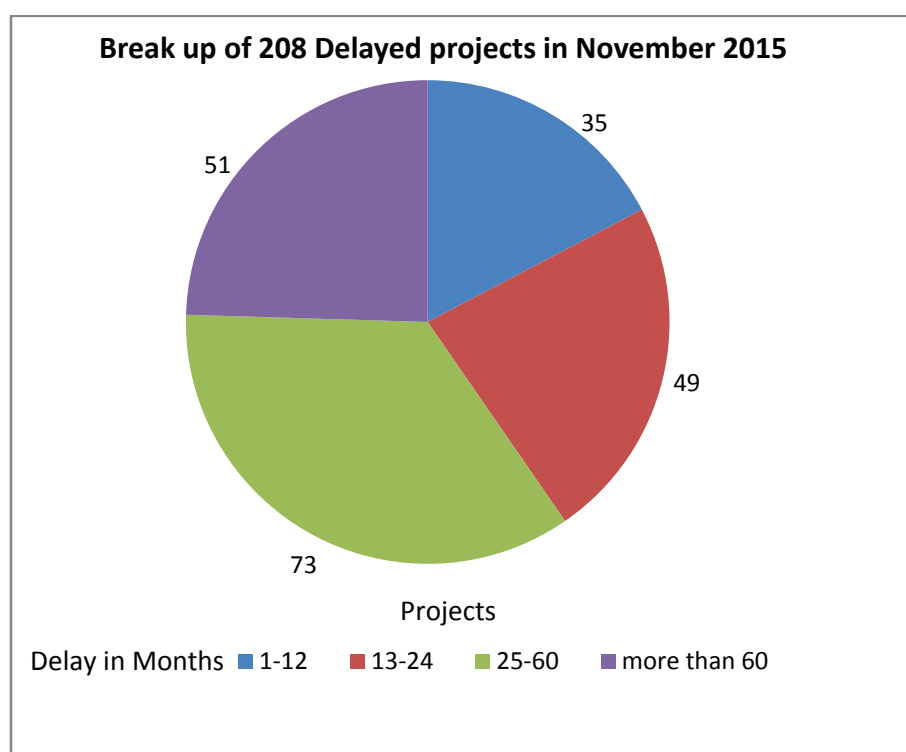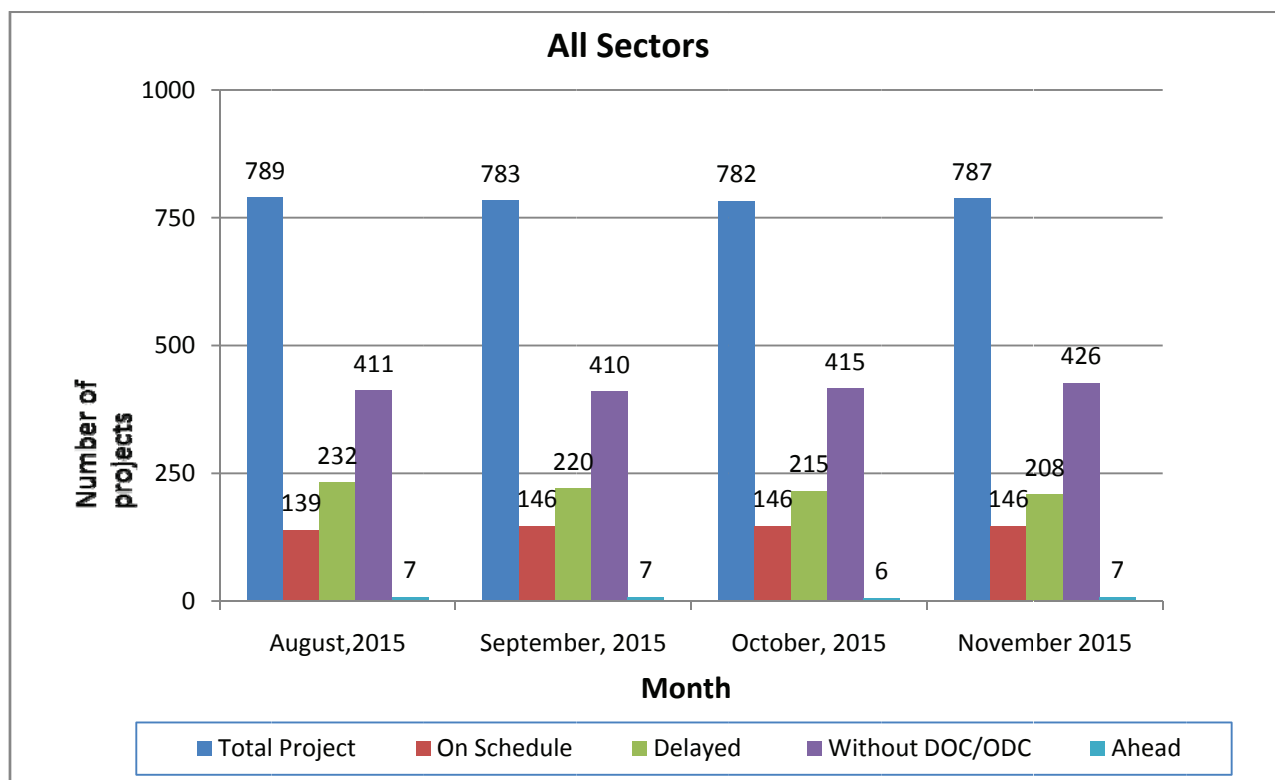



Graphical Presentation

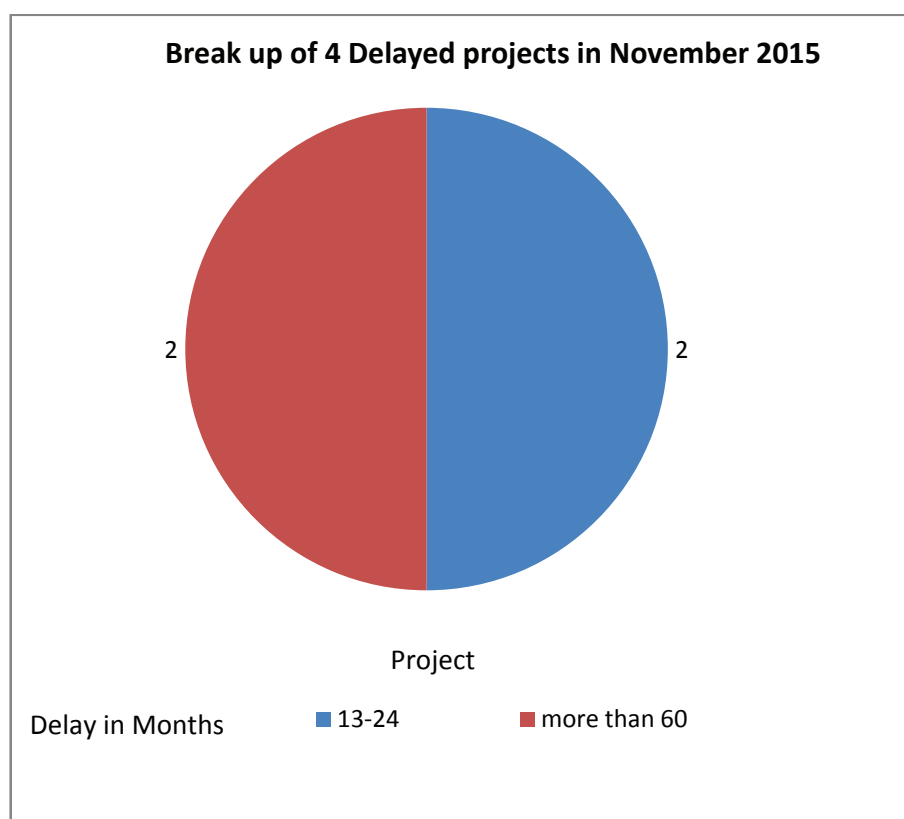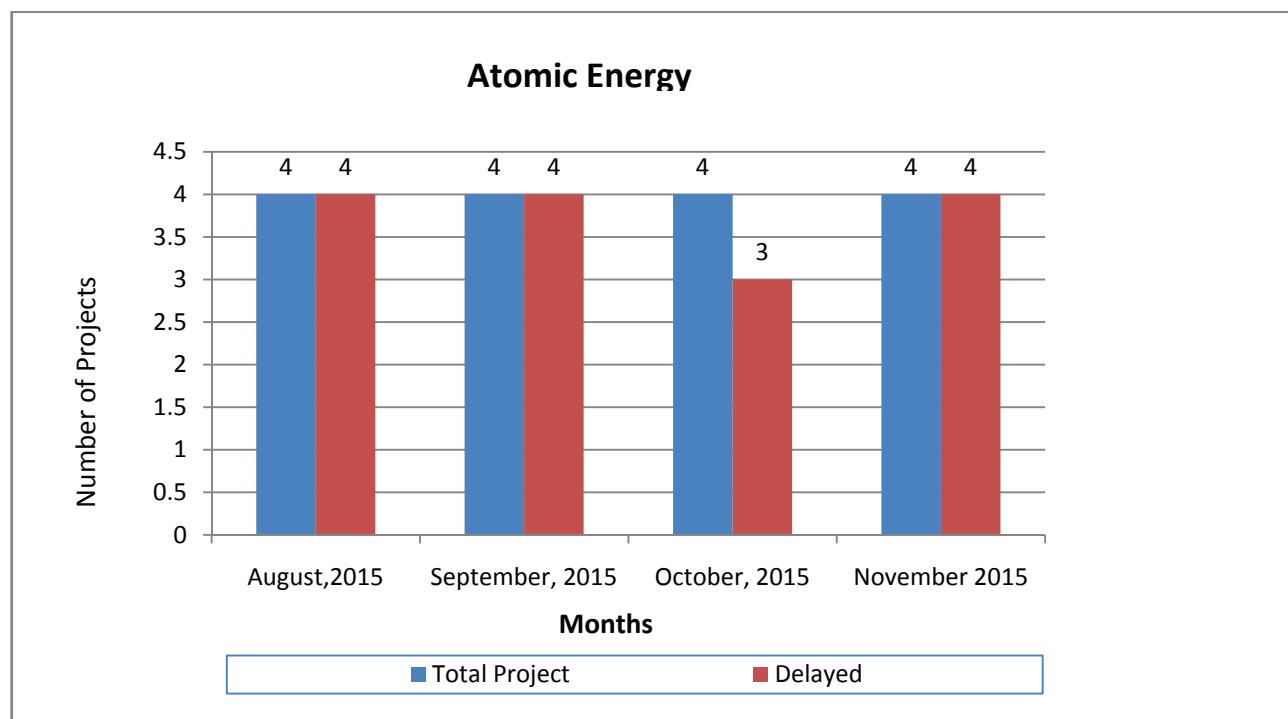



Graphical Presentation

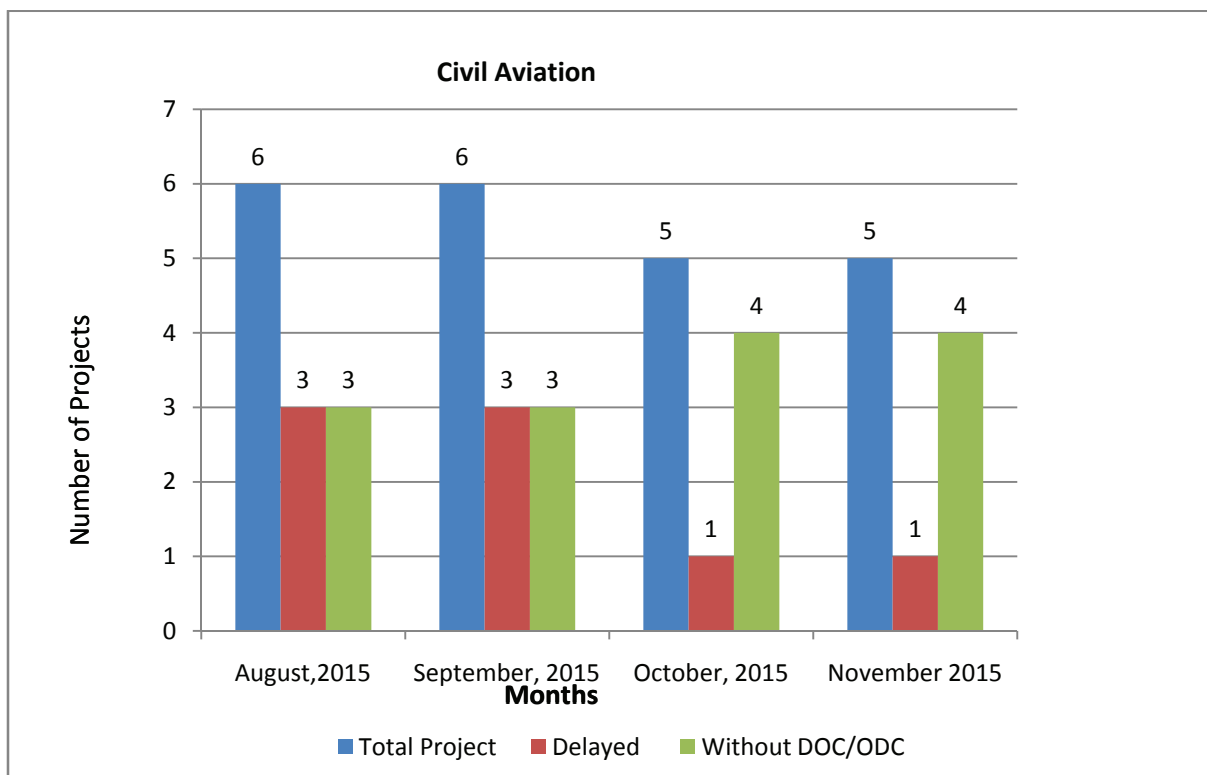



Graphical Presentation

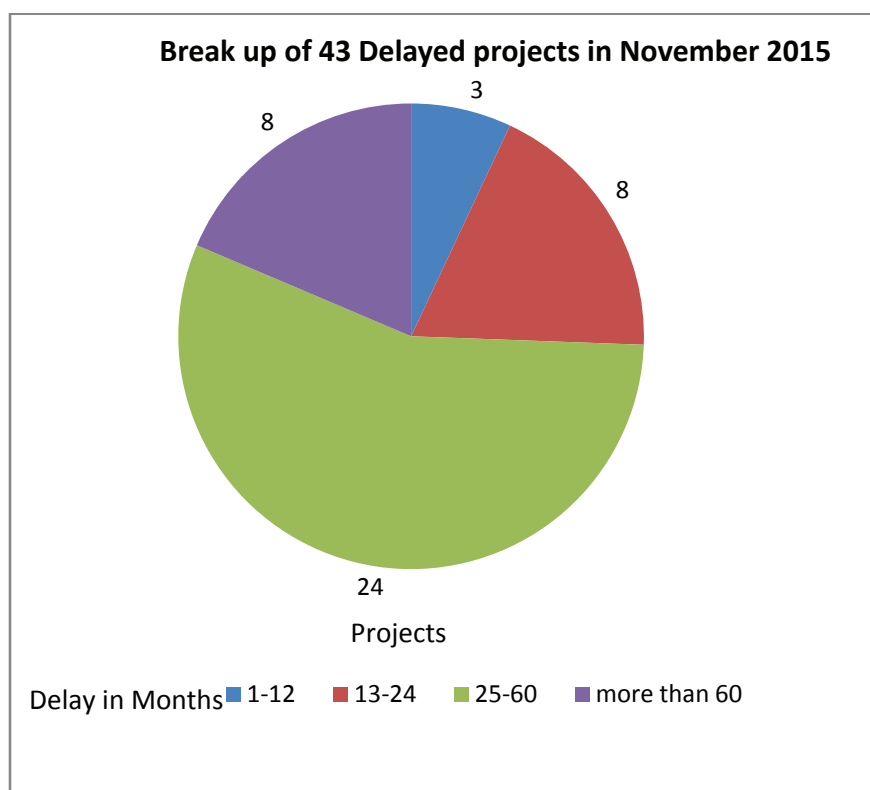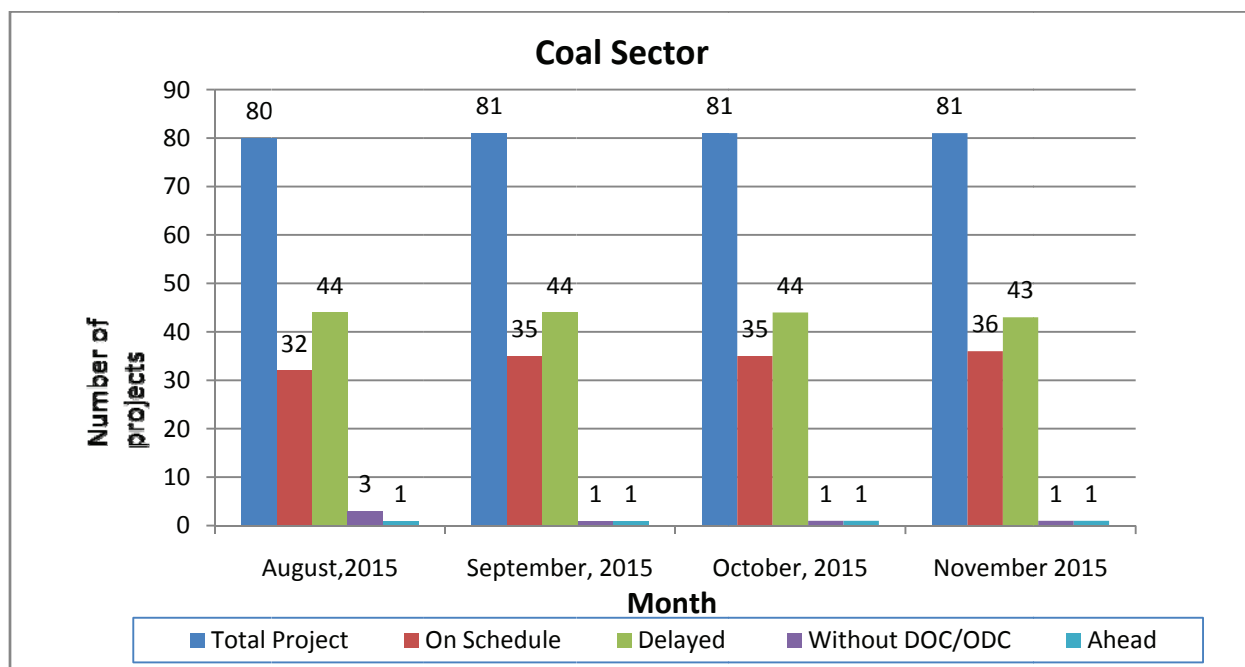



Graphical Presentation

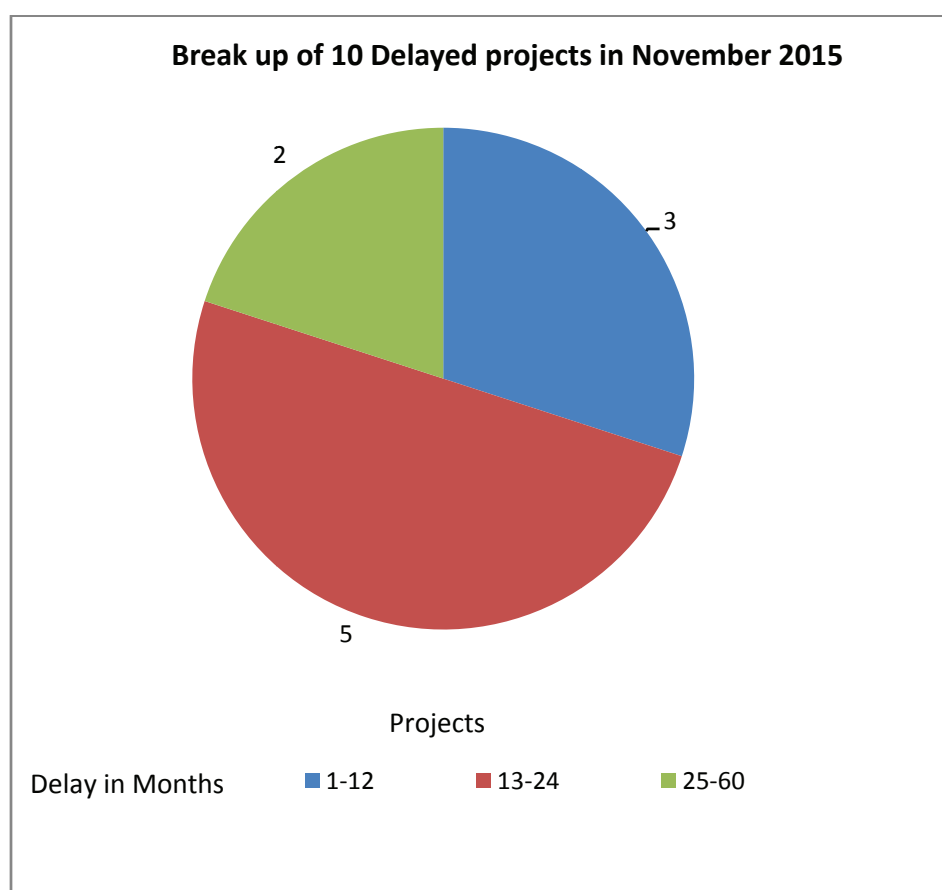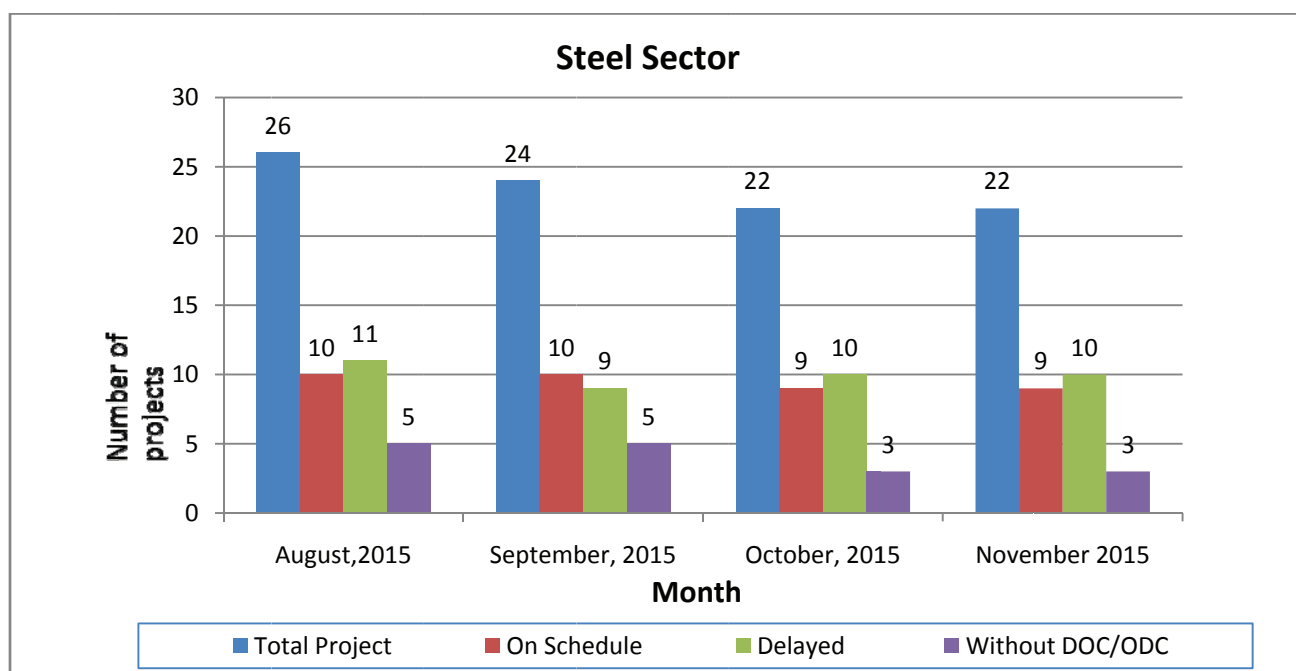



Graphical Presentation

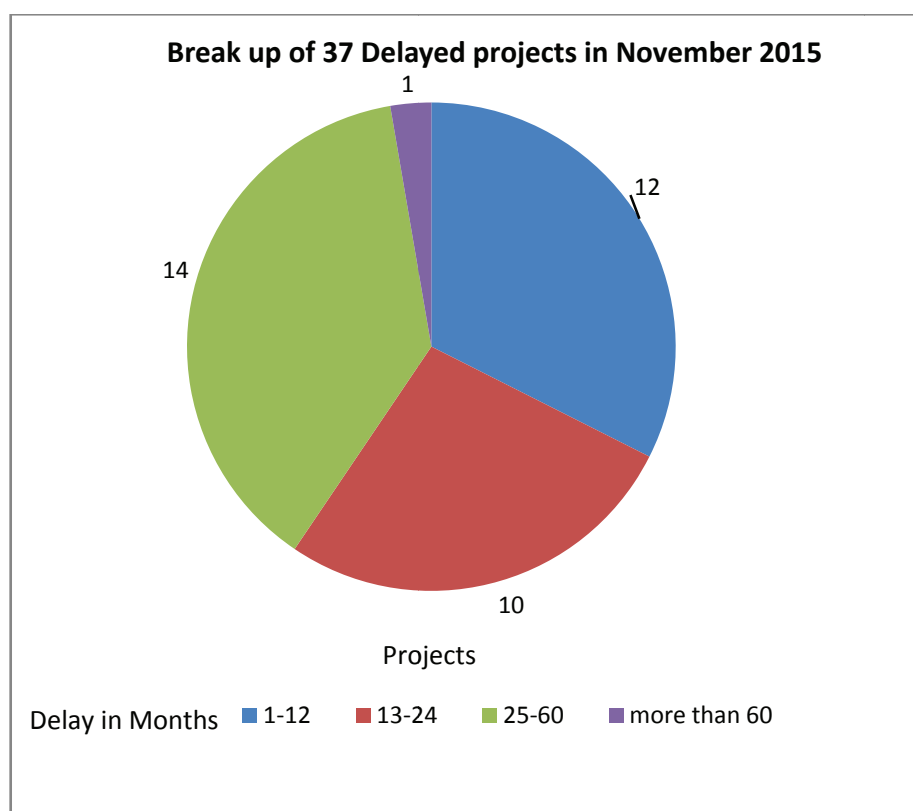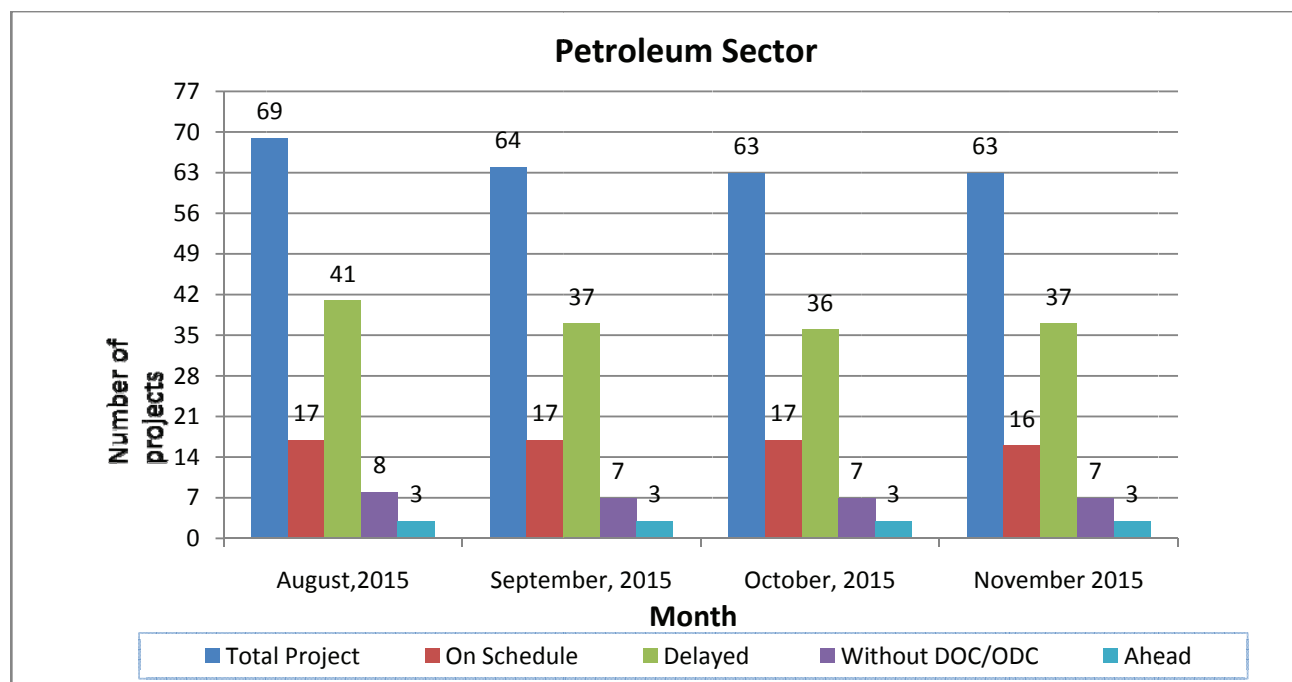

Graphical Presentation

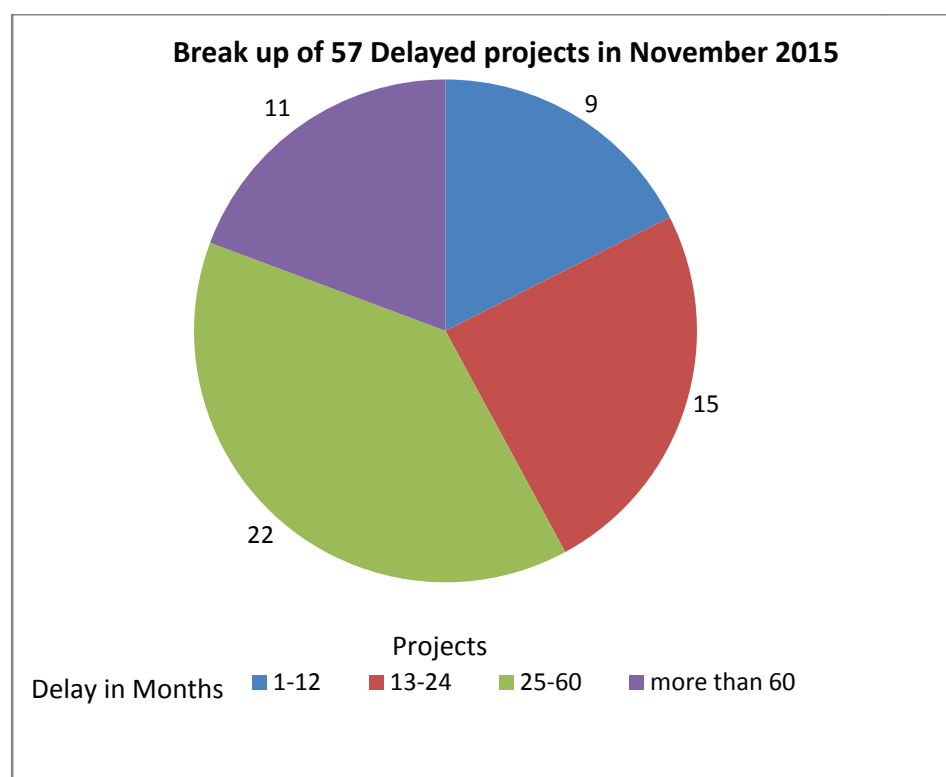
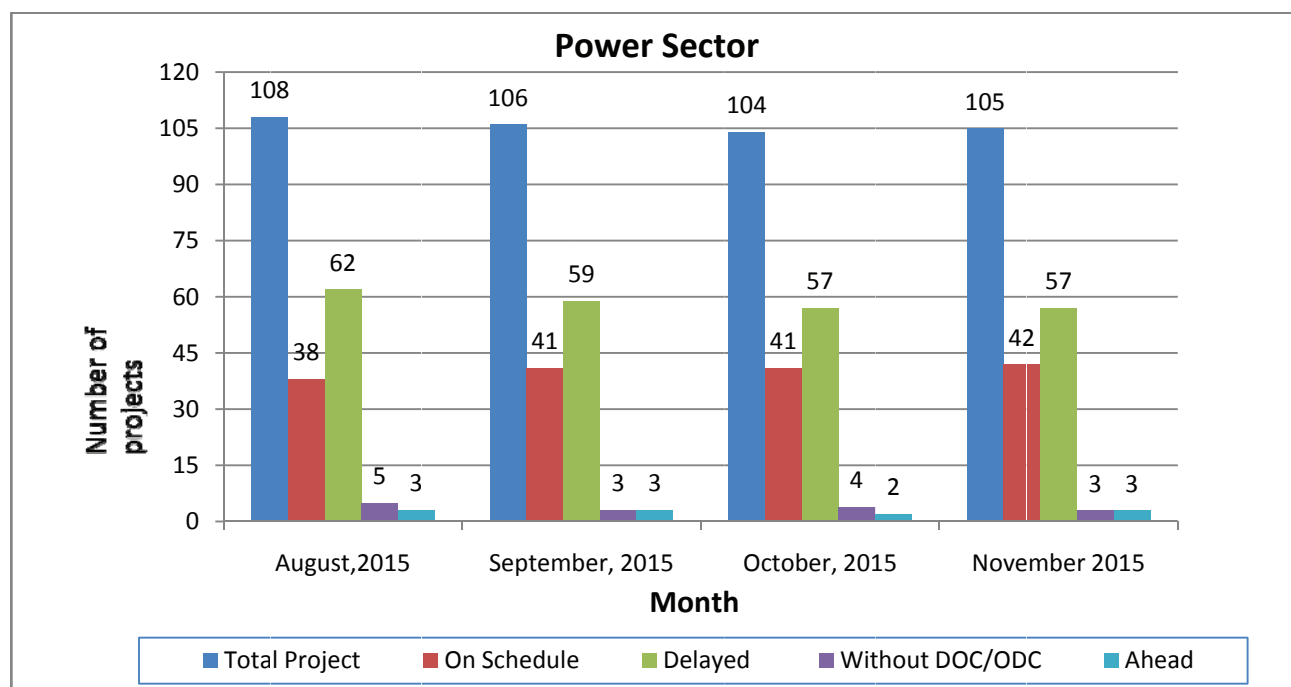


Graphical Presentation

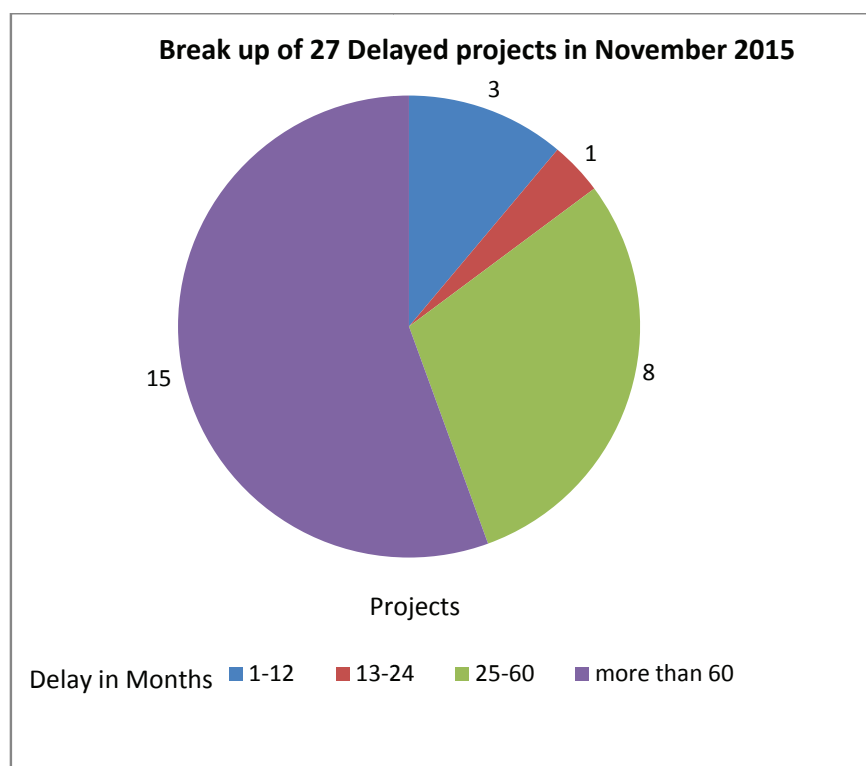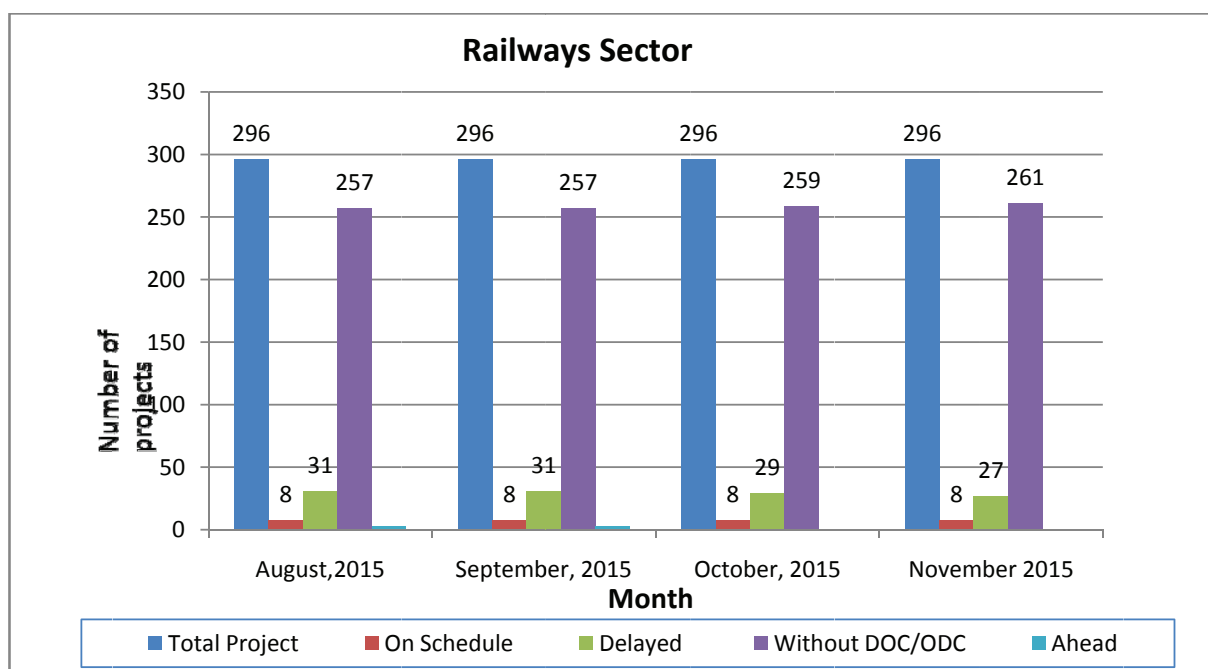



The Information in respect of Ministry of Railways is as on 01.01.2015. Ministry of Railways is not updating the information.

Graphical Presentation

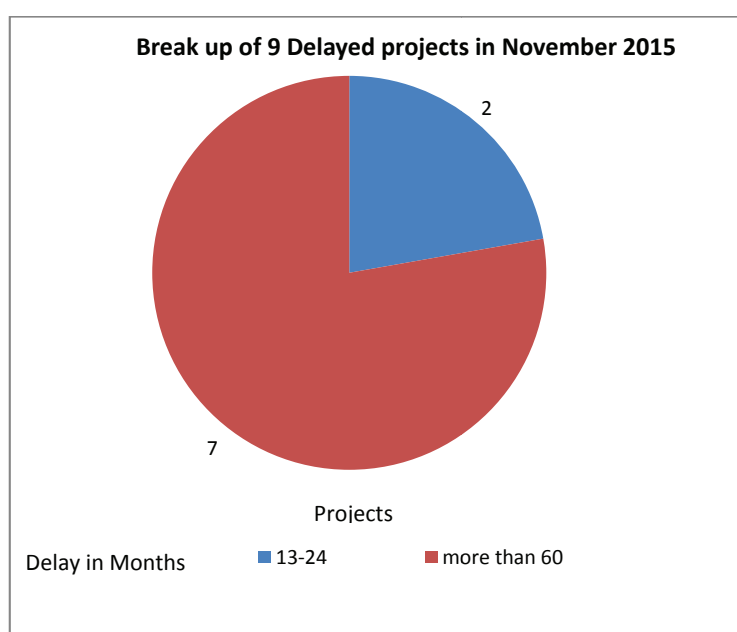
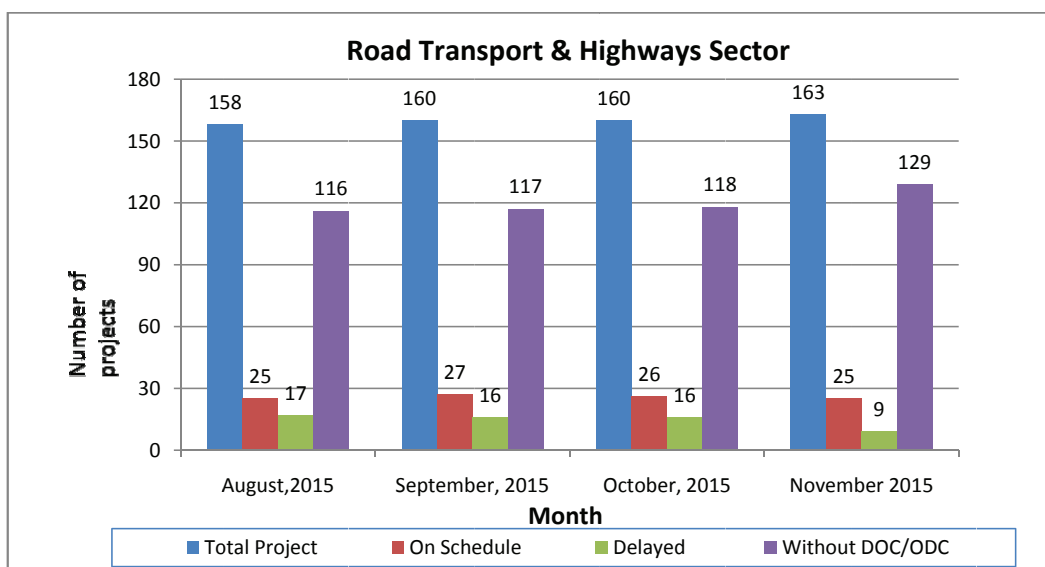


Out of 137 projects, the data / information of only 38 projects were submitted online by the NHAI for the month of September 2015. The data / information in respect of remaining projects is as per last reported data by NHAI.



Graphical Presentation

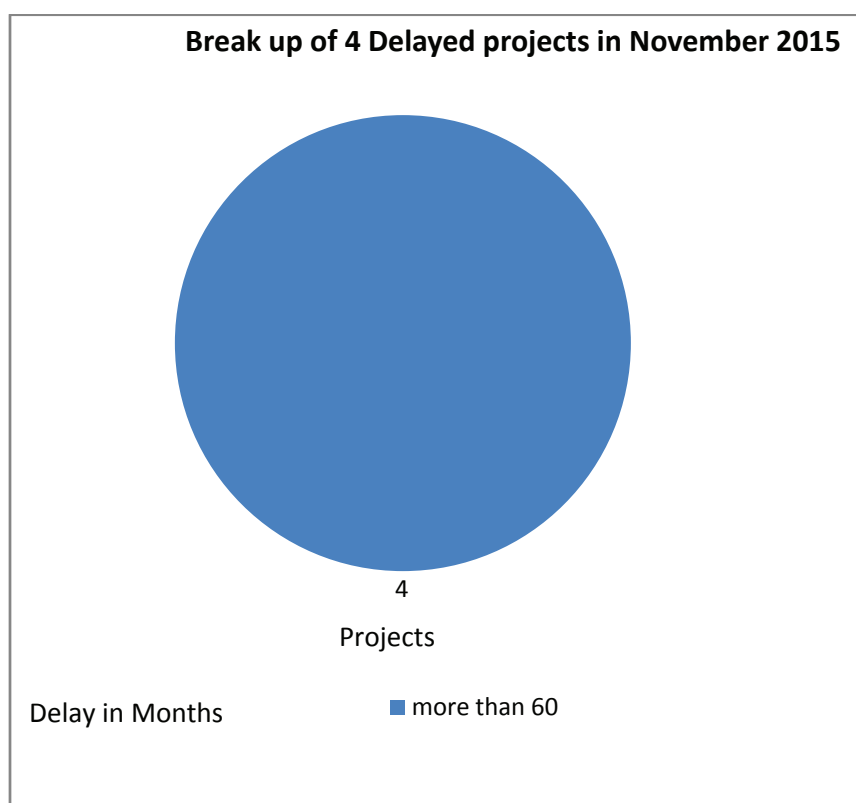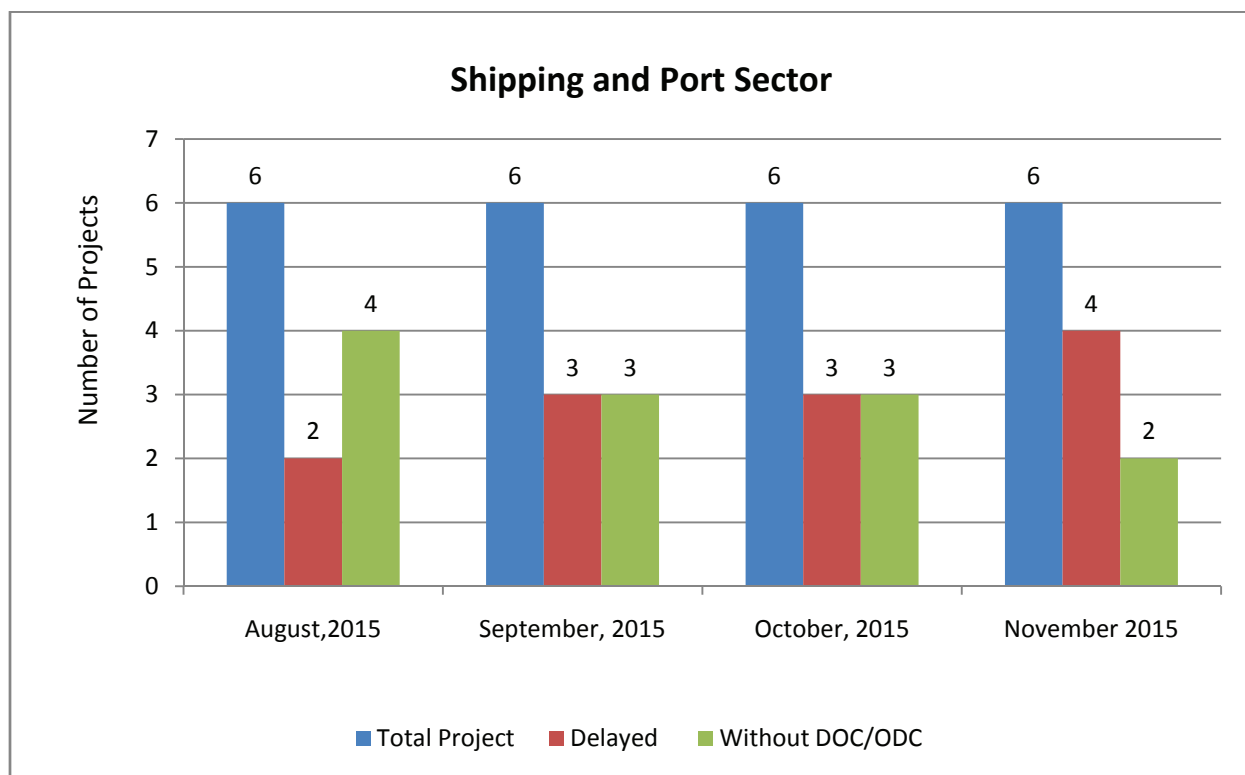



Graphical Presentation

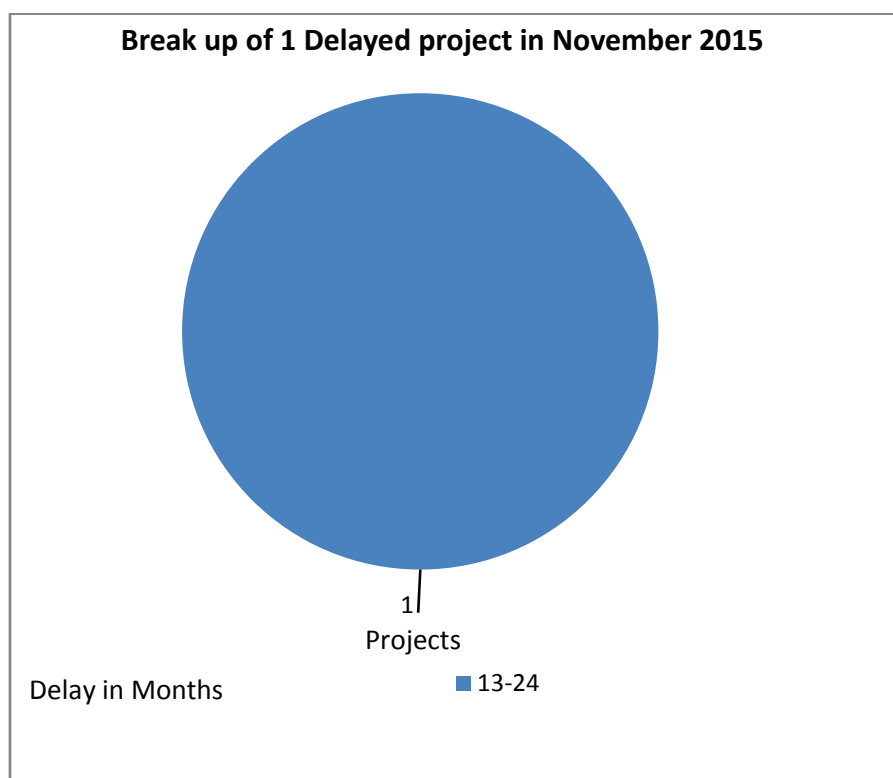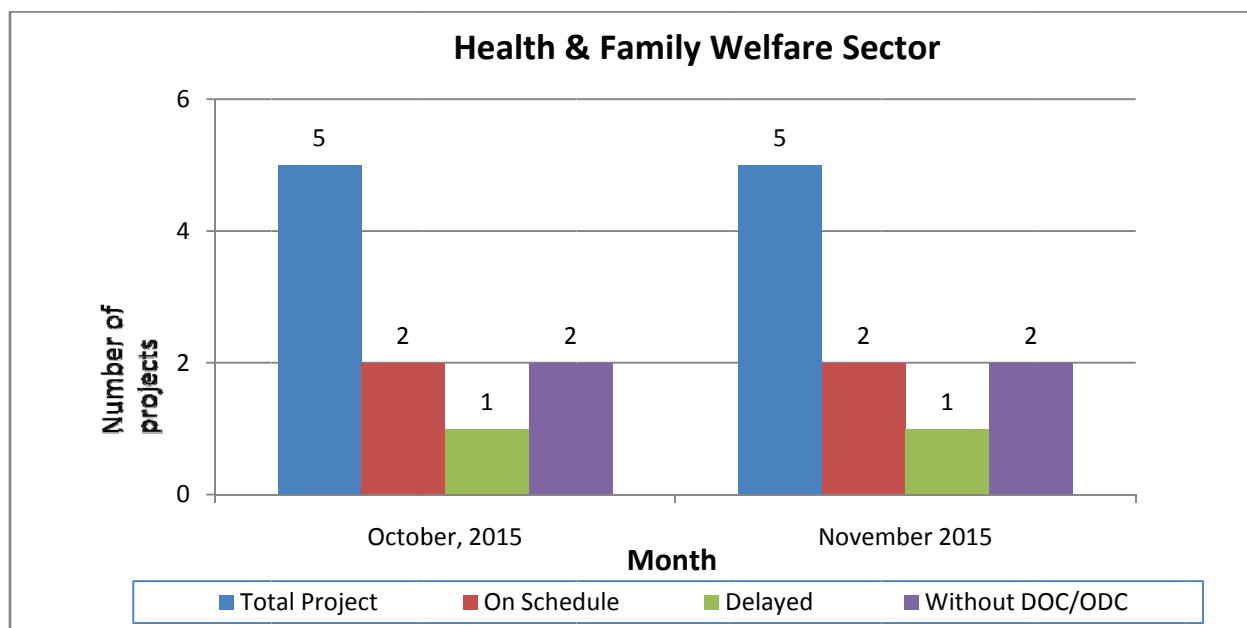

Graphical Presentation

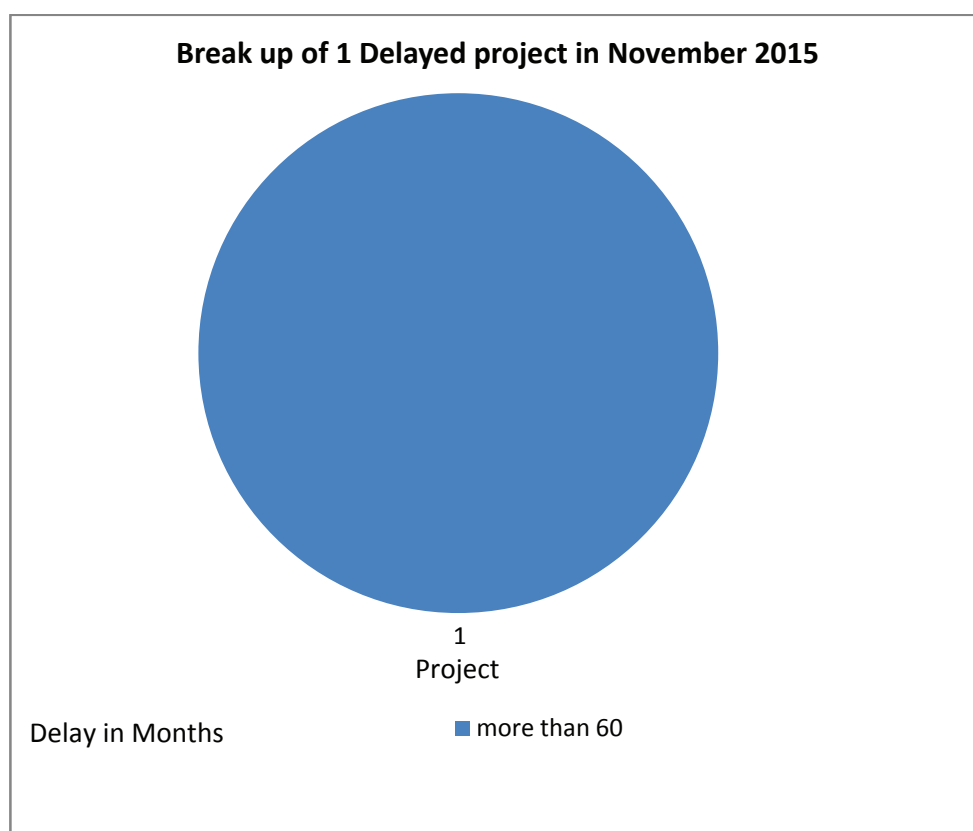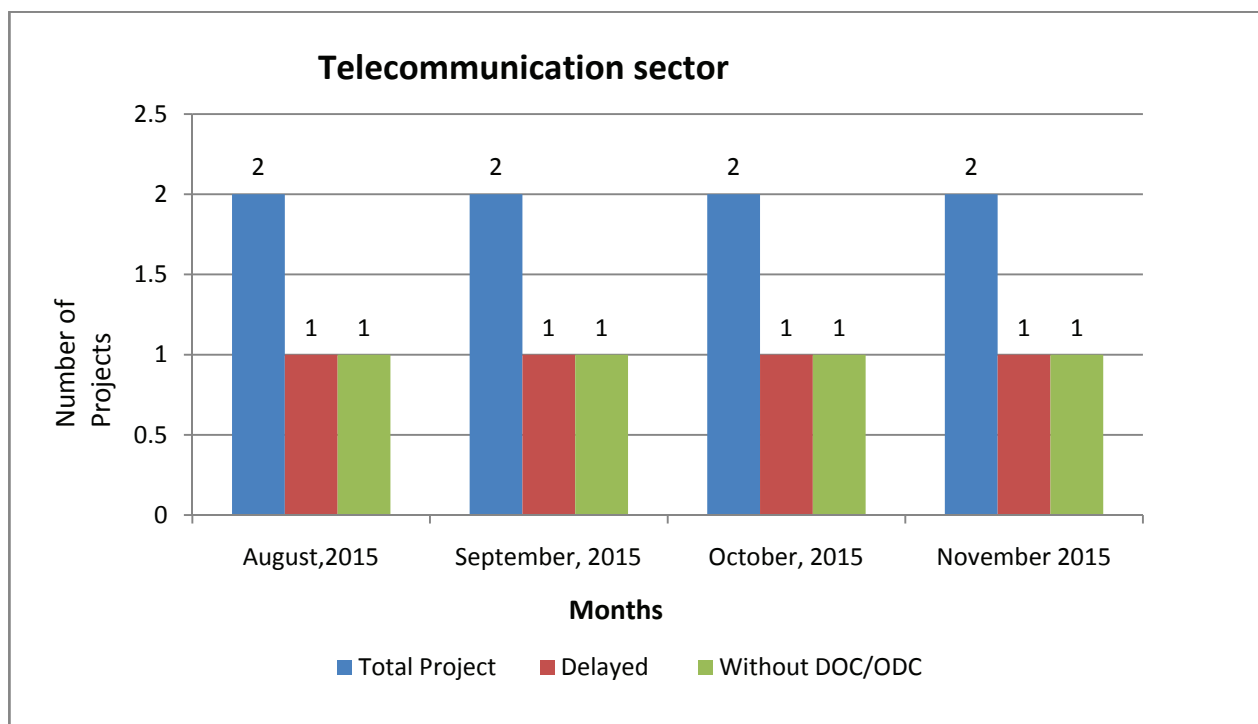

Graphical Presentation

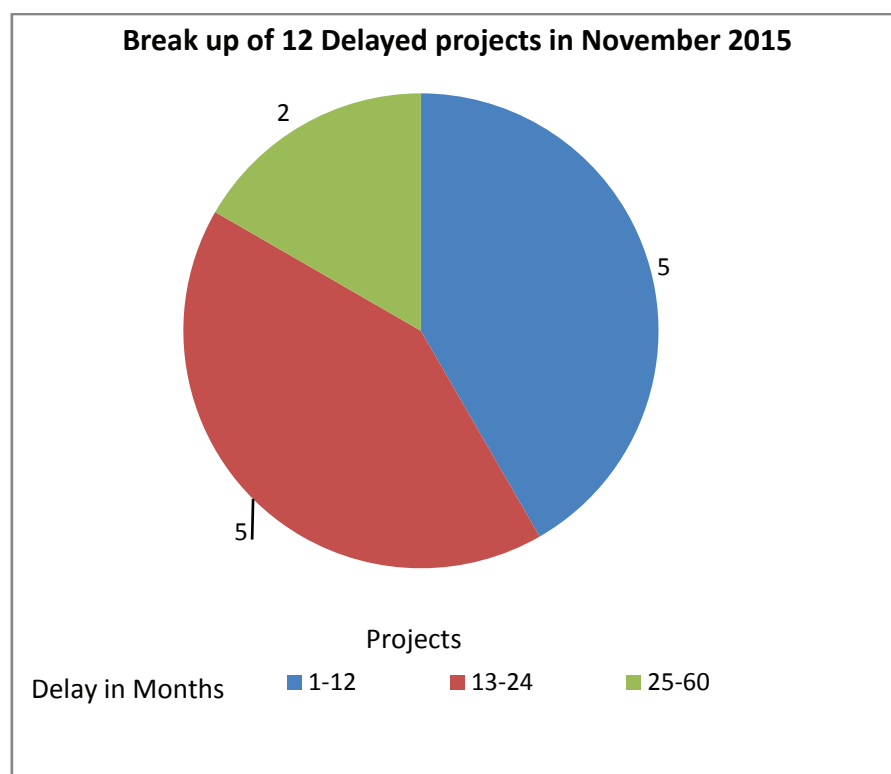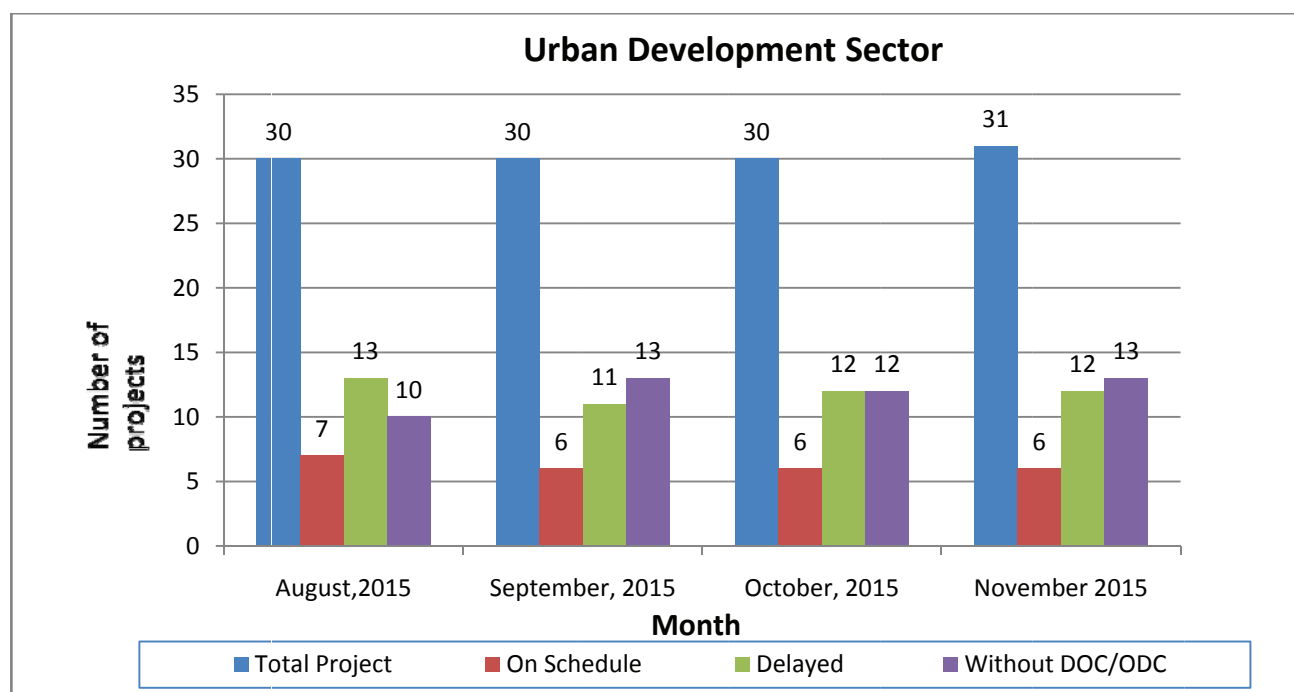

Sectorwise analysis of projects					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	40,442.00	44,541.00	51,918.00	33,718.00
CIVIL AVIATION	5	1,521.56	1,521.56	1,530.45	839.10
COAL	81	56,886.73	57,718.07	57,765.87	14,596.40
FERTILISERS	1	197.79	197.79	197.79	37.66
MINES	1	1,856.00	1,856.00	1,856.00	0.00
STEEL	22	49,833.99	49,833.99	49,979.39	26,805.47
PETROCHEMICALS	1	5,460.61	8,920.00	9,965.00	9,025.14
PETROLEUM	63	133,205.31	142,153.76	144,838.01	67,898.20
POWER	105	294,151.17	322,244.28	341,570.36	167,920.19
HEAVY INDUSTRY	1	1,718.00	1,718.00	3,827.30	0.00
HEALTH AND FAMILY WELFARE	5	1,390.58	1,390.58	1,390.58	619.70
RAILWAYS *	296	171,881.41	185,296.44	296,947.84	90,798.15
ROAD TRANSPORT AND HIGHWAYS **	163	106,445.00	106,768.14	108,621.05	38,176.70
SHIPPING AND PORTS	6	5,412.28	5,842.90	5,968.93	3,208.42
TELECOMMUNICATIONS	2	13,718.00	13,718.00	13,718.00	74.74
URBAN DEVELOPMENT	31	136,783.82	136,783.82	141,997.82	31,482.23
Grand total	787	1,020,904.25	1,080,504.33	1,232,092.39	485,200.10

* - Information in respect of Ministry of Railways is as on 01.01.2015. Ministry of Railways is not updating the information.

** - Out of 137 projects, the data / information of only 37 projects were submitted online by the NHAI for the month of November 2015. The data / information in respect of remaining projects is as per last reported data i.e. June 2015.

(All Cost/ Expenditure in Rs. Crore)

Sector Wise Details									
(November 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00	11,459.00	7,477.00	12/2015 10/2016	10/2017	22(O) 12(R)	40/70
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL, TAMIL NADU	12/2001	13,171.00 17,270.00	22,462.00	20,962.00	12/2008 10/2013	06/2016	90(O) 32(R)	54/102
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI, TAMIL NADU	09/2003	3,492.00	5,677.00	-	09/2010	09/2016	72(O)	12/88
4	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00	12,320.00	5,279.00	12/2016 04/2017	05/2018	17(O) 13(R)	28/69
	Total		40,442.00	51,918.00	33,718.00				134/329
	<u>CIVIL AVIATION</u>								
5	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI, SIKKIM	01/2009	309.46	309.46	404.81	01/2011 06/2016	09/2017	80(O) 15(R)	0/0
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, ANDAMAN & NICOBAR ISLANDS	10/2013	314.61	314.61	18.02	-	09/2018	-	0/0
7	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI, GOA	05/2010	335.61	318.00	305.01	05/2012	03/2015	-	0/0
8	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI, MULTI STATE	02/2010	344.28	344.28	80.60	03/2014	05/2015	-	0/0
9	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI, MULTI STATE	10/2012	217.60	244.10	30.66	03/2015	09/2015	-	0/0
	Total		1,521.56	1,530.45	839.10				0/0
	<u>COAL</u>								
10	ADASA UG TO OC - [N06000133]WCL, MAHARASHTRA	08/2015	288.90	288.90	-	03/2023	03/2023	0(O)	2/15
11	ADRIYALA SHAFT PROJECT - [N06000016]SCCL, TELANGANA	12/2009	212.34 1,228.39	1,228.39	861.82	03/2013 09/2012	03/2016	36(O) 42(R)	21/22
12	AMALGAMATED PAUNI-II III OC MINE - [N06000131]WCL, MAHARASHTRA	06/2015	483.69	483.69	31.57	03/2021	03/2021	0(O)	3/14
13	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]WCL, MAHARASHTRA	08/2015	727.28	727.28	51.53	03/2025	03/2025	0(O)	2/20
14	AMERA OC RCE - [N06000123]SECL, CHHATISGARH	02/2015	335.97	335.97	30.90	03/2018	03/2018	0(O)	0/4
15	AMGAON OPENCAST PROJECT RCE - [N06000135]SECL, CHHATISGARH	07/2015	316.10	316.10	15.85	03/2020	03/2020	0(O)	0/0
16	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL, CHHATISGARH	11/2009	150.59	198.59	122.91	03/2016	03/2016	0(O)	3/7

Sector Wise Details									
(November 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
17	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]NCL,MADHYA PRADESH	12/2009	1,352.04 1,143.54	1,143.54	808.39	03/2016 -	03/2016	0(O) -	4/4
18	AMRAPALI OC(12MTY) - [N06000103]CCL,JHARKHAND	02/2012	858.11 -	858.11	108.17	03/2020 -	03/2020	0(O) -	3/4
19	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH	02/2015	481.60 -	481.60	-	03/2023 -	03/2023	0(O) -	0/7
20	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	205.79	03/2012 -	03/2017	60(O) -	4/5
21	ASHOK EXPN OCP CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	341.63 -	341.63	126.41	03/2011 -	03/2017	72(O) -	2/5
22	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	150.27	03/2010 -	03/2017	84(O) -	2/4
23	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56 -	258.56	96.39	03/2016 -	03/2018	24(O) -	3/6
24	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA	05/2014	479.15 -	479.15	10.25	03/2019 -	03/2019	0(O) -	1/9
25	BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH	07/2015	231.92 -	231.92	-	03/2022 -	03/2022	0(O) -	0/0
26	BHANEKAON OC - [N06000121]WCL,MAHARASHTRA	02/2015	187.94 -	187.94	46.65	03/2023 -	03/2023	0(O) -	6/21
27	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.10 -	490.10	203.58	03/2017 -	03/2017	0(O) -	11/11
28	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL,CHHATISGARH	05/2014	164.49 -	164.49	76.43	03/2020 -	03/2020	0(O) -	2/6
29	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,MADHYA PRADESH	06/2011	746.04 535.10	535.10	412.91	03/2015 -	03/2016	12(O) -	3/3
30	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH	12/2013	610.63 -	610.33	-	03/2022 -	03/2022	0(O) -	1/7
31	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35 -	462.35	298.87	03/2014 -	03/2016	24(O) -	8/9
32	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	35.96	03/2011 -	03/2016	60(O) -	0/3
33	DINESH OCP - [N06000118]WCL,MAHARASHTRA	11/2014	611.16 -	611.16	116.97	03/2020 -	03/2020	0(O) -	3/15
34	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,701.89	03/2014 -	03/2016	24(O) -	11/13
35	DURGAPUR OPENCAST PROJECT - [N06000136]SECL,CHHATISGARH	02/2015	916.24 -	916.24	-	03/2023 -	03/2023	0(O) -	0/0
36	GARJANBAHAL OCP - [N06000117]MCL,ODISHA	11/2014	1,375.38 -	1,375.38	158.45	03/2021 -	03/2021	0(O) -	1/9
37	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,920.50	03/2014 -	03/2016	24(O) -	11/16
38	GOKUL - [N06000120]WCL,MAHARASHTRA	11/2014	267.67 -	267.67	176.11	03/2018 -	03/2018	0(O) -	2/18
39	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,ODISHA	02/2008	395.87 -	395.87	-	03/2015 -	03/2021	72(O) -	2/13
40	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	479.63	175.64	03/2013 -	03/2017	48(O) -	4/8
41	JAGANNATH RE-ORGANISATION OC,(6.00 MTY) - [N06000114]MCL,ODISHA	05/2014	337.66 -	337.66	0.29	03/2019 -	03/2019	0(O) -	2/6
42	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	152.43	24.72	03/2015 -	03/2020	60(O) -	1/7

Sector Wise Details									
(November 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
43	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL, TELANGANA	07/2011	447.06 -	447.06	29.03	03/2015 -	03/2018	36(O) -	4/13
44	JALLARAM SHAFT PROJECT - [N06000025]SCCL, TELANGANA	09/2007	467.78 -	467.78	2.85	03/2013 -	-	-	6/83
45	JHANJRA R-VI SEAM PSLW - [N06000020]ECL, WEST BENGAL	11/2006	287.18 -	287.18	226.26	03/2011 -	03/2017	72(O) -	9/15
46	KAKATIYA LONGWALL - [N06000048]SCCL, TELANGANA	12/2008	453.63 -	453.63	101.64	12/2012 -	03/2017	51(O) -	11/44
47	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]SCCL, TELANGANA	05/2015	397.09 -	397.09	-	03/2019 -	03/2019	0(O) -	5/18
48	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL, TELANGANA	07/2012	417.33 -	417.33	14.13	07/2016 -	03/2017	8(O) -	6/28
49	KANCHAN OC EXPANSION - [N06000125]SECL, MADHYA PRADESH	12/2014	371.04 -	371.04	28.78	03/2021 -	03/2021	0(O) -	0/6
50	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL, ODISHA	12/2007	457.77 -	457.77	206.83	03/2013 -	03/2017	48(O) -	8/9
51	KAPURIA UG(PSLW) - [N06000108]BCCL, JHARKHAND	08/2011	988.35 -	988.35	45.27	04/2017 -	04/2017	0(O) -	0/2
52	KARMA OCP (1.0MTY) - [N06000088]CCL, JHARKHAND	06/2009	162.46 -	162.46	70.05	03/2014 -	03/2017	36(O) -	3/4
53	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH	07/2008	178.44 -	178.44	0.30	03/2014 -	03/2020	72(O) -	1/7
54	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA, 6MTPA INCREMENTAL) - [N06000091]NCL, UTTAR PRADESH	06/2011	1,131.28 1,131.28	1,131.28	125.67	03/2018 -	03/2018	0(O) -	4/4
55	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29 -	242.29	0.03	03/2015 -	03/2018	36(O) -	0/5
56	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL, UTTAR PRADESH	06/2011	789.88 741.62	741.62	493.43	03/2013 -	03/2016	36(O) -	2/2
57	KULDA EXPN OC, (5.00 MTY) - [N06000115]MCL, ODISHA	06/2014	289.03 -	289.03	-	03/2018 -	03/2018	0(O) -	1/5
58	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL, ODISHA	01/2005	302.96 -	302.96	297.02	03/2010 -	03/2016	72(O) -	8/10
59	KUSMUNDA EXPN. OCP(SECL)(15-50)MTY - [N06000008]SECL, CHHATISGARH	08/2013	7,612.33 7,612.33	7,612.33	783.81	03/2023 03/2023	03/2023	0(O) 0(R)	1/17
60	MADHUBAND NLW WASHERY - [N06000126]BCCL, JHARKHAND	08/2010	289.45 -	289.45	98.72	05/2014 -	10/2016	29(O) -	0/8
61	MAGADH OC 20 MTY (CCL) - [N06000015]CCL, JHARKHAND	08/2008	706.40 -	706.40	77.72	07/2012 -	03/2021	104(O) -	1/3
62	MAKARDHOKRA I OC - [N06000119]WCL, MAHARASHTRA	09/2014	266.23 -	266.23	92.30	03/2021 -	03/2021	0(O) -	3/22
63	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH	12/2009	321.50 -	321.50	209.59	03/2014 -	03/2018	48(O) -	4/7
64	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL, TELANGANA	03/2010	181.19 -	181.19	64.25	03/2012 -	03/2016	48(O) -	5/6
65	MOONIDIH XV SEAM UG - [N06000098]BCCL, JHARKHAND	08/2011	1,230.27 -	1,230.27	47.76	04/2015 04/2019	04/2019	48(O) 0(R)	2/11
66	MURADIH UG TURN-KEY PROJECT - [N06000096]BCCL, JHARKHAND	02/2011	339.88 -	339.88	12.06	04/2014 -	03/2016	23(O) -	4/7
67	NEW MAJRI UG TO OC - [N06000128]WCL, MAHARASHTRA	05/2015	295.56 -	295.56	79.02	03/2019 -	03/2019	0(O) -	4/20

Sector Wise Details									
(November 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
68	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 -	5,907.11	1,204.77	12/2015 04/2018	04/2018	28(O) 0(R)	11/35
69	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 486.57	486.57	59.23	03/2012 03/2018	03/2017	60(O) -12(R)	2/2
70	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND	02/2014	555.52 -	555.52	3.52	03/2021 -	03/2017	-48(O) -	0/2
71	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	-	03/2012 -	03/2017	60(O) -	3/3
72	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	269.82	55.36	04/2014 -	11/2016	31(O) -	0/10
73	PELMA OCP(15.00MTY) - [N06000045]SECL,CHHATISGARH	11/2014	1,624.59 1,624.59	1,624.59	5.43	03/2023 03/2023	03/2023	0(O) 0(R)	1/10
74	PENGANGA OCP(REVISED) - [N06000066]WCL,MAHARASHTRA	09/2014	441.82 -	441.82	127.86	03/2020 -	03/2020	0(O) -	5/27
75	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	-	03/2013 -	03/2016	36(O) -	4/4
76	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	67.34	03/2014 -	03/2016	24(O) -	3/9
77	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH	12/2014	357.80 -	357.80	108.44	03/2021 -	03/2021	0(O) -	0/7
78	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	224.44	03/2016 -	03/2016	0(O) -	2/4
79	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	418.97	365.11	03/2012 -	03/2016	48(O) -	0/2
80	RAMPUR BATURA OCP (4.0 MTY) - [N06000049]SECL,MADHYA PRADESH	08/2015	1,186.64 -	1,186.64	1.33	03/2023 -	03/2023	0(O) -	1/6
81	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	162.76	1.31	03/2015 -	03/2019	48(O) -	4/29
82	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 486.27	486.27	93.51	03/2016 -	03/2016	0(O) -	7/39
83	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	6.56	06/2015 -	03/2017	21(O) -	18/51
84	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78 -	209.78	73.19	03/2015 -	03/2016	12(O) -	8/31
85	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	249.03	76.65	03/2012 -	03/2018	72(O) -	29/42
86	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA	05/2014	3,756.36 -	3,756.36	620.40	03/2026 -	03/2026	0(O) -	3/15
87	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05 -	1,055.05	191.06	03/2018 -	03/2018	0(O) -	1/10
88	TALABIRA OCP - [N06000043]MCL,ODISHA	03/2008	447.72 -	447.72	52.36	03/2016 -	03/2020	48(O) -	2/11
89	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	-	03/2012 -	03/2016	48(O) -	2/4
90	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]NLC,TAMIL NADU	04/2012	364.75 -	364.75	182.79	10/2014 -	03/2016	17(O) -	8/10
	Total		56,886.73 -	57,765.87	14,596.40				324/1010

Sector Wise Details									
(November 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>FERTILISERS</u>								
91	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF, MAHARASHTRA	10/2014	197.79 197.79	197.79	37.66	11/2016 -	11/2016	0(0) -	0/0
	Total		197.79 -	197.79	37.66				0/0
	<u>MINES</u>								
92	EXPANSION OF MALANJKHAND MINE- DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]JCL, MADHYA PRADESH	09/2011	1,856.00 -	1,856.00	-	09/2017 -	09/2017	0(0) -	0/0
	Total		1,856.00 -	1,856.00	.00				0/0
	<u>STEEL</u>								
93	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC, KARNATAKA	04/2011	572.00 -	572.00	480.37	04/2013 09/2014	06/2015	-	18/19
94	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL, JHARKHAND	10/2013	245.67 -	245.67	68.15	05/2016 -	05/2016	0(0) -	1/3
95	3RD CONVERTER AND 4TH CASTER - [N12000088]RINL, ANDHRA PRADESH	07/2011	974.76 -	974.76	197.53	07/2016 -	07/2016	0(0) -	0/1
96	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC, KARNATAKA	02/2011	898.55 -	898.55	405.22	05/2013 01/2015	08/2015	-	19/20
97	ALTERNATE GAS NETWORK AT BSL - [N12000093]SAIL, JHARKHAND	03/2015	255.19 -	255.19	22.05	03/2018 -	03/2018	0(0) -	0/0
98	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL, ANDHRA PRADESH	07/2011	877.73 -	877.73	332.82	07/2015 -	06/2016	11(0) -	2/2
99	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH - [N12000078]SAIL, CHHATISGARH	07/2012	332.65 -	332.65	222.78	08/2014 -	01/2016	17(0) -	4/5
100	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL, CHHATISGARH	04/2014	188.93 -	188.93	51.77	04/2015 -	-	-	1/4
101	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, CHHATISGARH	08/2010	17,265.00 -	17,265.00	15,279.06	03/2013 -	06/2016	39(0) -	31/35
102	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL, JHARKHAND	02/2014	4,749.00 -	4,749.00	1.29	09/2017 -	09/2017	0(0) -	0/0
103	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL, MAHARASHTRA	12/2011	187.33 -	187.33	171.52	10/2013 -	03/2016	29(0) -	2/6
104	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL, ODISHA	10/2012	160.48 -	160.48	142.58	09/2014 -	12/2015	15(0) -	2/3
105	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL, ODISHA	04/2015	3,127.30 -	3,127.30	156.76	04/2018 -	04/2018	0(0) -	0/0
106	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL, JHARKHAND	05/2015	1,154.18 -	1,154.18	17.72	12/2017 -	12/2017	0(0) -	0/0
107	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL, JHARKHAND	03/2015	1,034.01 -	1,034.01	-	10/2017 -	10/2017	0(0) -	0/0

Sector Wise Details									
(November 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
108	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC, CHHATISGARH	01/2010	15,525.00 -	15,525.00	8,195.12	05/2015 12/2016	12/2016	19(O) 0(R)	18/81
109	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]SAIL, WEST BENGAL	11/2012	313.05 -	313.05	301.82	06/2015 -	12/2015	6(O) -	3/4
110	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079]SAIL, ODISHA	06/2012	237.09 -	237.09	216.21	12/2014 -	01/2016	13(O) -	2/3
111	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL, ANDHRA PRADESH	12/2009	343.00 -	488.40	33.61	10/2016 -	10/2016	0(O) -	0/0
112	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL, ANDHRA PRADESH	05/2012	404.16 -	404.16	248.15	07/2015 -	03/2017	20(O) -	0/1
113	TURBO BLOWER - 5 - [N12000092]RINL, ANDHRA PRADESH	12/2009	280.00 -	280.00	15.77	09/2016 -	09/2016	0(O) -	1/1
114	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]SAIL, ODISHA	06/2014	708.91 -	708.91	245.17	04/2016 -	08/2016	4(O) -	2/2
	Total		49,833.99 -	49,979.39	26,805.47				106/190
	<u>PETROCHEMICALS</u>								
115	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, ASSAM	04/2006	5,460.61 8,920.00	9,965.00	9,025.14	04/2012 12/2013	12/2015	44(O) 24(R)	21/26
	Total		5,460.61 -	9,965.00	9,025.14				21/26
	<u>PETROLEUM</u>								
116	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]ONGC, MULTI STATE	03/2014	2,476.82 -	2,476.82	368.95	12/2018 -	12/2018	0(O) -	3/9
117	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, ASSAM	03/2009	2,465.15 2,378.89	2,378.89	1,789.38	03/2013 03/2016	03/2017	48(O) 12(R)	5/15
118	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL, MULTI STATE	08/2011	586.00 -	586.00	400.66	08/2015 -	12/2015	4(O) -	0/12
119	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL, MULTI STATE	01/2015	1,823.00 -	1,823.00	0.86	- -	-	-	0/0
120	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]GAIL, ANDHRA PRADESH	07/2014	419.04 -	419.04	240.86	01/2017 -	06/2016	-7(O) -	11/16
121	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC, MULTI STATE	06/2007	736.65 -	736.65	498.95	09/2011 12/2015	06/2016	57(O) 6(R)	0/0
122	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC, GUJARAT	03/2009	317.64 -	240.95	123.32	09/2012 12/2015	03/2016	42(O) 3(R)	0/5
123	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC, ASSAM	06/2010	202.94 -	202.94	2.95	01/2014 -	-	-	0/2
124	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC, MAHARASHTRA	03/2011	861.79 1,256.72	1,256.72	989.16	05/2013 12/2015	04/2016	35(O) 4(R)	1/5
125	CRU TO ISOMERIZATION (ISOM) - [N16000200]BPCL, MULTI STATE	10/2011	725.00 -	725.00	80.59	11/2016 -	12/2016	1(O) -	0/14
126	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC, D & N HAVELI	08/2014	6,086.08 -	6,086.08	586.87	05/2019 03/2020	03/2020	10(O) 0(R)	0/0

Sector Wise Details									
(November 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
127	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA	12/2009	1,584.00 -	1,584.00	1,353.89	08/2015 -	03/2016	7(O) -	0/12
128	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 2,592.17	2,592.17	826.62	05/2014 05/2016	05/2016	24(O) 0(R)	0/21
129	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC,MULTI STATE	04/2013	284.82 -	284.82	-	04/2015 05/2017	05/2017	25(O) 0(R)	0/5
130	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17 600.17	600.17	375.14	12/2014 05/2015	05/2016	17(O) 12(R)	0/8
131	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE	06/2010	2,523.00 2,523.00	2,523.00	1,658.41	01/2014 12/2015	12/2015	23(O) 0(R)	0/13
132	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]ONGC,MULTI STATE	10/2013	429.06 429.00	429.06	439.02	10/2014 10/2015	11/2015	13(O) 1(R)	0/0
133	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL	03/2014	3,076.00 -	3,076.00	112.15	09/2017 -	12/2017	3(O) -	0/0
134	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	711.00	7.42	- -	-	-	0/0
135	GAMJI REDEVELOPMENT PROJECT - [N16000202]ONGC,GUJARAT	05/2015	1,671.22 1,881.22	1,881.22	-	11/2019 -	11/2019	0(O) -	0/0
136	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]IOCL,ASSAM	02/2014	163.88 -	163.88	46.91	07/2016 -	07/2016	0(O) -	4/6
137	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	1,282.07	03/2015 05/2016	05/2016	14(O) 0(R)	0/17
138	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]ONGC,MAHARASHTRA	12/2012	3,513.07 4,619.94	4,619.94	667.40	02/2016 12/2017	12/2017	22(O) 0(R)	0/0
139	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE	05/2013	4,124.35 4,941.49	4,941.49	521.23	04/2016 12/2017	12/2017	20(O) 0(R)	0/6
140	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL,KERALA	03/2012	14,225.00 -	16,504.00	9,087.43	05/2016 -	05/2016	0(O) -	0/30
141	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE	01/2012	352.49 -	352.49	131.19	03/2014 05/2016	05/2016	26(O) 0(R)	0/3
142	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE	02/2015	890.00 -	890.00	0.76	- -	-	-	0/0
143	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00 -	2,915.00	1,378.43	12/2012 -	06/2015	-	7/14
144	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	10/2015	607.06 714.25	714.25	59.42	10/2017 10/2017	10/2017	0(O) 0(R)	21/48
145	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,KARNATAKA	02/2012	666.00 838.08	838.08	546.07	11/2015 11/2016	11/2016	12(O) 0(R)	25/29
146	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL,ODISHA	07/2009	199.75 -	239.73	205.75	07/2013 11/2015	11/2015	28(O) 0(R)	0/1
147	MARKETING TOP AT KORBA - [N16000186]IOCL,CHHATISGARH	01/2011	141.86 -	232.00	159.09	09/2016 -	03/2016	-6(O) -	0/12
148	MH NORTH REDEVELOPMENT PHASE III - [N16000188]ONGC,MAHARASHTRA	06/2014	5,706.47 5,813.25	5,813.25	2,268.83	05/2017 05/2017	05/2017	0(O) 0(R)	6/16
149	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL,TAMIL NADU	12/2012	279.00 -	279.00	186.74	12/2014 -	12/2015	12(O) -	57/58

Sector Wise Details									
(November 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
150	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA	11/2014	6,068.80 -	6,068.80	523.70	04/2019 -	03/2019	-1(O) -	0/0
151	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA	08/2015	2,818.88 -	2,818.88	-	03/2019 -	03/2019	0(O) -	0/0
152	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL,TAMIL NADU	05/2015	257.87 -	257.87	33.94	11/2016 -	11/2016	0(O) -	7/22
153	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	171.83	-	- -	-	- -	0/0
154	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	913.00	455.18	08/2015 -	12/2016	16(O) -	0/0
155	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00 -	2,321.00	1.50	- -	-	- -	0/0
156	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	15.00	07/2018 -	07/2018	0(O) -	1/31
157	PARADIP REFINERY PROJECT - [N16000058]IOCL,ODISHA	02/2009	29,777.00 34,555.00	34,555.00	30,413.42	11/2012 11/2013	01/2016	38(O) 26(R)	92/100
158	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	1,250.50	09/2012 -	03/2016	42(O) -	6/7
159	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]IOCL,ODISHA	03/2014	238.50 -	238.50	1.07	03/2017 -	03/2017	0(O) -	0/0
160	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	3,957.00 3,561.00	3,561.00	24.73	01/2013 -	12/2018	71(O) -	8/38
161	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC,MAHARASHTRA	02/2015	2,899.93 -	2,899.93	502.37	05/2017 -	05/2017	0(O) -	0/0
162	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT	09/2011	202.25 -	160.16	68.96	07/2016 -	07/2016	0(O) -	5/12
163	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	3,150.00	110.77	09/2017 -	09/2017	0(O) -	0/0
164	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	251.66	-	06/2012 11/2015	01/2016	43(O) 2(R)	0/0
165	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 686.58	686.58	540.72	04/2015 04/2015	05/2016	13(O) 13(R)	0/0
166	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL,MAHARASHTRA	03/2012	1,419.00 -	1,419.00	1,284.80	12/2014 -	11/2015	11(O) -	0/20
167	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]IOCL,BIHAR	04/2013	480.00 -	480.00	85.08	02/2016 -	07/2016	5(O) -	2/6
168	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU	02/2011	3,110.36 -	3,110.36	1,211.76	11/2015 07/2016	07/2016	8(O) 0(R)	44/52
169	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96 -	191.96	96.98	05/2015 -	12/2015	7(O) -	0/12
170	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL,GUJARAT	12/2011	160.00 -	160.00	31.28	02/2016 02/2016	03/2016	1(O) 1(R)	0/0
171	REWARI KANPUR PIPELINE PROJECT - [N16000145]HPCL,MULTI STATE	02/2012	1,210.64 1,446.34	1,446.34	1,249.03	11/2015 -	11/2015	0(O) -	24/24
172	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	450.55	10.60	03/2017 -	03/2017	0(O) -	0/0
173	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	1,016.37	10/2011 -	03/2016	53(O) -	0/0

Sector Wise Details

(November 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
174	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]SPRL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,438.30	01/2012 -	03/2016	50(O) -	0/0
175	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM	03/2009	228.64 -	214.19	135.00	12/2016 -	12/2016	0(O) -	0/0
176	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	1,200.00	432.84	03/2015 11/2015	08/2016	17(O) 9(R)	0/5
177	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 462.79	462.79	253.37	10/2014 03/2017	03/2017	29(O) 0(R)	28/40
178	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	463.32	314.41	06/2011 03/2012	03/2016	57(O) 48(R)	13/20
	Total		133,205.31 -	144,838.01	67,898.20				370/766
	POWER								
179	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 -	155.57	1.00	03/2016 -	03/2016	0(O) -	0/6
180	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 15,095.67	15,095.67	11,012.00	01/2011 10/2014	05/2018	88(O) 43(R)	27/48
181	BOKARO THERMAL POWER STATION-A - [N18000199]DVC,JHARKHAND	08/2006	2,313.00 4,139.00	4,237.67	3,088.00	12/2011 -	03/2016	51(O) -	0/0
182	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 6,749.18	6,749.18	5,588.00	09/2011 -	03/2017	66(O) -	17/37
183	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	5,353.00	5,129.27	05/2014 -	09/2017	40(O) -	0/4
184	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	1,043.56	12/2015 -	12/2016	12(O) -	15/18
185	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,864.76	09/2014 -	06/2016	21(O) -	8/13
186	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	956.42	06/2015 -	08/2016	14(O) -	3/5
187	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,ANDHRA PRADESH	03/2012	206.44 -	206.44	43.97	06/2014 -	-	-	11/20
188	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	277.30	06/2015 -	08/2016	14(O) -	7/10
189	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	1,394.52	-	05/2017 -	05/2017	0(O) -	0/9
190	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL,DELHI	05/2015	780.33 -	780.33	-	07/2017 -	07/2017	0(O) -	0/0
191	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA	02/2014	12,532.44 -	12,532.44	2,151.00	08/2018 -	08/2018	0(O) -	16/16

Sector Wise Details									
(November 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
192	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 -	195.42	40.43	02/2014 -	09/2017	43(O) -	1/1
193	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 -	196.58	5.10	02/2016 -	06/2016	4(O) -	5/17
194	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	1,219.55	11/2012 -	12/2016	49(O) -	8/13
195	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	1,364.52	430.87	04/2016 -	04/2016	0(O) -	8/12
196	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 -	522.29	47.20	11/2016 -	11/2016	0(O) -	0/12
197	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	90.74	09/2014 -	06/2016	21(O) -	0/0
198	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	197.40	-	03/2018 -	03/2018	0(O) -	0/0
199	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATTISGARH	05/2011	1,961.87 -	1,961.87	1,757.69	05/2014 -	06/2016	25(O) -	8/12
200	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH	07/2013	3,363.12 -	3,363.12	882.00	12/2016 -	12/2016	0(O) -	14/17
201	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	03/2013	11,638.55 -	11,638.55	4,480.00	09/2017 -	09/2017	0(O) -	18/41
202	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]PGCIL,MULTI STATE	04/2015	1,479.30 -	1,479.30	60.62	04/2017 -	04/2017	0(O) -	2/8
203	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE	04/2015	3,705.61 -	3,705.61	138.53	04/2018 -	04/2018	0(O) -	4/9
204	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL,MULTI STATE	07/2015	2,247.37 -	2,247.37	15.10	07/2018 -	07/2018	0(O) -	0/0
205	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]PGCIL,MULTI STATE	05/2014	303.07 -	303.07	19.70	07/2016 -	07/2016	0(O) -	2/9
206	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24 -	1,071.24	-	09/2017 -	09/2017	0(O) -	0/0
207	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]PGCIL,MULTI STATE	12/2014	6,517.36 -	6,517.36	231.99	04/2018 -	04/2018	0(O) -	3/12
208	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 6,476.34	6,476.34	4,252.71	12/2009 12/2016	12/2016	84(O) 0(R)	16/27
209	KBUNL-MUZAFFARPUR TPP STAGE-II- SUBSIDIARY (2X195 MW) - [N18000191]NTPC,BIHAR	03/2010	3,984.03 -	3,984.03	3,096.26	01/2013 -	03/2016	38(O) -	0/1
210	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,497.72	4,276.75	01/2016 -	11/2016	10(O) -	6/9
211	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	01/2012	15,166.19 -	15,166.19	9,676.00	01/2017 -	03/2017	2(O) -	29/35
212	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	2,159.07	1,897.65	11/2008 03/2012	12/2016	97(O) 57(R)	20/22
213	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATTISGARH	12/2012	11,846.00 -	11,846.00	5,137.00	06/2017 -	06/2017	0(O) -	20/40

Sector Wise Details									
(November 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
214	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00	1,527.00	142.00	08/2017	08/2017	0(O)	0/9
215	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47	7,921.47	4,704.00	09/2016	09/2016	0(O)	27/32
216	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89	9,750.89	4,233.50	12/2016	09/2017	9(O)	25/28
217	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58	14,366.58	2,241.00	02/2019	02/2019	0(O)	9/10
218	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 13,762.80	13,762.80	11,184.10	08/2013 12/2017	12/2017	52(O) 0(R)	16/26
219	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL,MULTI STATE	02/2014	908.08	908.08	114.91	06/2016	06/2016	0(O)	9/18
220	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 689.03	689.03	515.20	07/2013 11/2015	06/2016	35(O) 7(R)	7/9
221	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29	410.29	342.05	02/2012	12/2015	46(O)	7/10
222	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66	509.66	500.24	11/2011	06/2016	55(O)	8/11
223	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82	539.82	100.76	06/2016	06/2016	0(O)	8/11
224	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57	1,677.57	1,436.11	04/2013	01/2016	33(O)	8/11
225	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63	723.63	554.56	11/2014	06/2016	19(O)	7/10
226	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL,MULTI STATE	09/2013	680.69	680.69	421.64	03/2016	03/2016	0(O)	10/12
227	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40	524.40	269.39	05/2015	01/2016	8(O)	8/12
228	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58	965.58	753.44	11/2012	01/2016	38(O)	7/10
229	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60	12,964.60	4,609.32	01/2018	01/2018	0(O)	21/24
230	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]NHPC,JAMMU AND KASHMIR	10/2014	8,112.12	8,112.12	-	04/2020	04/2020	0(O)	0/0
231	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59	7,818.68	5,328.26	09/2009	12/2018	111(O)	10/14
232	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99 1,487.49	1,487.49	1,074.08	08/2013 05/2016	05/2016	33(O) 0(R)	28/38
233	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN,BIHAR	05/2015	436.68	436.68	398.45	12/2016	12/2016	0(O)	0/1
234	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]DVC,WEST BENGAL	04/2007	4,122.00 8,781.00	9,606.82	1,353.36	02/2011	01/2017	71(O)	0/0
235	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL	09/2014	1,381.84	1,381.84	149.00	09/2019	09/2019	0(O)	2/3
236	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18	9,395.18	5,620.00	11/2016	08/2017	9(O)	25/27
237	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE	05/2014	829.98	829.98	64.00	08/2016	08/2016	0(O)	0/4

Sector Wise Details									
(November 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
238	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]PGCIL,KARNATAKA	02/2014	167.40 -	167.40	84.40	12/2015 -	12/2015	0(O) -	5/8
239	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]PGCIL,MULTI STATE	11/2014	972.42 -	972.42	-	11/2017 -	11/2017	0(O) -	0/3
240	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	18,063.89	7,870.78	09/2010 -	-	-	0/0
241	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]PGCIL,ANDHRA PRADESH	03/2015	550.06 -	550.06	1.60	03/2018 -	03/2018	0(O) -	0/3
242	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE	08/2014	288.49 -	288.49	48.40	02/2017 -	02/2017	0(O) -	0/12
243	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHHATTISGARH - [N18000116]PGCIL,CHHATTISGARH	12/2011	1,746.65 2,228.71	2,228.71	1,475.50	08/2014 12/2015	06/2016	22(O) 6(R)	7/11
244	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,060.56	08/2012 -	03/2016	43(O) -	3/5
245	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]PGCIL,MULTI STATE	02/2014	243.53 -	243.53	185.63	08/2016 -	12/2015	-8(O) -	8/10
246	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 -	203.28	18.38	07/2017 -	07/2017	0(O) -	0/5
247	SYSTEM STRENGTHENING XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	232.34	199.00	06/2012 -	-	-	1/4
248	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATTISGARH	01/2012	1,422.85 -	1,422.85	1,349.97	01/2015 -	06/2016	17(O) -	9/11
249	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 346.79	346.79	289.16	08/2014 06/2015	02/2016	18(O) 8(R)	8/10
250	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 639.46	639.46	412.96	06/2014 03/2016	11/2015	17(O) -4(R)	10/12
251	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH	09/2014	9,188.98 -	9,188.98	891.00	03/2019 -	03/2019	0(O) -	10/15
252	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	2,631.00	03/2013 -	12/2018	69(O) -	2/15
253	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]NHPC, WEST BENGAL	09/2005	1,061.38 -	1,929.15	1,923.42	09/2009 -	06/2016	81(O) -	2/6
254	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	1,498.91	02/2016 02/2016	09/2019	43(O) 43(R)	8/21
255	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	2,301.62	08/2014 -	02/2016	18(O) -	8/14
256	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAND AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	2,869.07	10/2014 -	06/2016	20(O) -	8/17
257	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	4,181.23	10/2012 -	12/2016	50(O) -	7/11
258	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]PGCIL,GUJARAT	02/2014	378.71 -	378.71	113.06	10/2016 -	10/2016	0(O) -	8/11

Sector Wise Details									
(November 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
259	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]PGCIL,MULTI STATE	01/2015	268.80 -	268.80	20.32	03/2018 -	03/2018	0(O) -	0/3
260	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL,MULTI STATE	02/2012	1,927.16 -	1,927.16	1,564.24	10/2014 -	01/2016	15(O) -	11/15
261	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]PGCIL,MULTI STATE	06/2014	400.47 -	400.47	45.19	04/2017 -	04/2017	0(O) -	0/3
262	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL,MULTI STATE	09/2013	1,575.30 -	1,575.30	623.05	05/2016 -	05/2016	0(O) -	8/13
263	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	2,219.30	12/2012 -	06/2016	42(O) -	11/23
264	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN	07/2015	307.18 -	307.18	0.80	11/2017 -	11/2017	0(O) -	0/0
265	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE	01/2015	871.62 -	871.62	1.90	10/2017 -	10/2017	0(O) -	0/5
266	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]PGCIL,ANDHRA PRADESH	08/2014	188.75 -	188.75	70.77	02/2017 -	03/2016	-11(O) -	0/2
267	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	546.58	02/2014 -	12/2015	22(O) -	8/10
268	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 -	4,404.57	2,357.96	01/2015 -	12/2016	23(O) -	8/16
269	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	489.81	11/2013 -	02/2016	27(O) -	8/12
270	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 2,348.37	2,348.37	1,914.09	03/2013 06/2015	01/2016	34(O) 7(R)	8/11
271	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	184.17	01/2013 -	01/2016	36(O) -	10/15
272	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,536.72	11/2013 -	03/2016	28(O) -	8/12
273	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH-PART A (PHASE-I) - [N18000198]PGCIL,ANDHRA PRADESH	05/2015	312.94 -	312.94	2.11	05/2016 -	05/2016	0(O) -	0/0
274	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHHATTISGARH - [N18000112]PGCIL,CHHATTISGARH	11/2011	2,127.51 -	2,127.51	2,287.68	07/2014 -	06/2016	23(O) -	6/8
275	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	5,151.37	702.99	03/2018 -	03/2018	0(O) -	8/12
276	TRIPURA GAS BASED POWER PROJECT - [N18000071]NPEPCO,TRIPURA	07/2009	421.01 1,007.57	1,007.57	947.62	07/2013 12/2015	12/2015	29(O) 0(R)	25/26

Sector Wise Details									
(November 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
277	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM	07/1998	368.72 1,381.71	1,381.71	910.21	07/2006 10/2017	10/2017	135(O) 0(R)	5/13
278	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	5.36	04/2016 -	11/2016	7(O) -	0/0
279	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	2,491.58	752.82	06/2013 -	12/2019	78(O) -	4/8
280	WARDHA-HYDERABAD 765 KV LINK - [N18000183]PGCIL,MULTI STATE	01/2015	3,662.02 -	3,662.02	295.06	05/2018 -	05/2018	0(O) -	0/5
281	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 721.81	721.81	555.26	09/2010 06/2013	06/2016	69(O) 36(R)	4/8
282	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203]NHPC,RAJASTHAN	02/2015	302.49 302.00	302.49	147.75	02/2016 -	12/2015	-2(O) -	0/1
283	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATTISGARH	03/2012	9,569.76 -	9,569.76	5,312.24	06/2015 -	06/2016	12(O) -	20/30
	Total		294,151.17 -	341,570.36	167,920.19				766/1268
	HEAVY INDUSTRY								
284	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]HIPE,MULTI STATE	04/2011	1,718.00 -	3,827.30	-	09/2011 -	12/2017	75(O) -	0/0
	Total		1,718.00 -	3,827.30	.00				0/0
	HEALTH AND FAMILY WELFARE								
285	AIIMS-RAEBARELI-HOUSING - [N21000006]HSCC,UTTAR PRADESH	10/2013	159.50 -	159.50	92.88	11/2013 -	09/2015	-	0/0
286	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	175.57	89.92	12/2014 -	03/2016	15(O) -	0/0
287	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	414.11	208.71	11/2013 -	11/2014	-	0/0
288	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS - SUPER SPECIALITY BLOCK - [N21000004]HSCC,DELHI	09/2013	444.70 -	444.70	228.19	12/2015 -	12/2015	0(O) -	0/0
289	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT & OTHERS-EMERGENCY BLOCK - [N21000005]HSCC,DELHI	11/2013	196.70 -	196.70	-	01/2016 -	01/2016	0(O) -	0/0
	Total		1,390.58 -	1,390.58	619.70				0/0
	RAILWAYS*								
290	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP,TELANGANA	04/2012	632.68 -	816.55	48.00	03/2016 -	03/2016	0(O) -	0/0
291	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]JR,MAHARASHTRA	04/2011	184.06 -	184.06	15.23	- -	-	-	0/0
292	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 813.34	2,876.00	823.83	03/2014 -	03/2018	48(O) -	0/0

Sector Wise Details									
(November 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
293	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	252.00 -	886.65	-	-	03/2018	-	0/0
294	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	432.72	436.85	12/2009 03/2011	06/2015	-	0/0
295	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	567.18	31.99	-	-	-	0/0
296	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	385.60	83.50	03/2013 -	-	-	0/0
297	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	2,820.00	329.67	-	-	-	0/0
298	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	873.71	-	-	-	-	0/0
299	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	218.39	23.63	-	-	-	0/0
300	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	822.00	-	-	-	-	0/0
301	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE	04/2008	184.26 -	2,000.00	17.32	-	-	-	0/0
302	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE	12/2006	170.00 -	485.00	417.70	03/2011 -	-	-	0/0
303	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	242.09	0.39	-	-	-	0/0
304	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	338.54	129.14	-	-	-	0/0
305	AMBAR FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	312.12 257.93	453.10	134.79	-	03/2018	-	0/0
306	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 663.01	725.00	586.75	06/1999 -	07/2012	-	0/0
307	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	295.68	0.86	-	-	-	0/0
308	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	307.00	-	-	-	-	0/0
309	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	1,566.00	137.40	-	-	-	0/0
310	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	490.80	0.39	-	-	-	0/0
311	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	304.41	0.19	-	-	-	0/0
312	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA	03/2015	960.00 -	960.00	-	-	-	-	0/0
313	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	528.00	2.96	-	-	-	0/0
314	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	199.75	76.08	-	-	-	0/0
315	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	986.30	100.76	-	-	-	0/0
316	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	288.35	9.60	-	-	-	0/0

Sector Wise Details

(November 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
317	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL	04/1999	207.52 -	207.52	223.44	12/2012 -	09/2015	-	0/0
318	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR, KARNATAKA	04/1996	138.00 -	1,382.78	2.81	- -	-	-	0/0
319	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR, RAJASTHAN	04/2012	246.08 -	246.08	4.20	- -	-	-	0/0
320	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	2,371.85	486.25	03/2005 12/2008	12/2019	177(O) 132(R)	0/0
321	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	1,106.62 -	1,106.62	244.99	12/2010 -	-	-	0/0
322	BARIAPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER, MULTI STATE	04/2007	450.55 -	450.55	13.53	- -	-	-	0/0
323	BAZAR SAU - AZIMGANJ N. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64 -	255.64	-	- -	-	-	0/0
324	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP) - [220100164]MRTP, MAHARASHTRA	03/1996	495.44 495.44	1,781.98	440.08	03/2004 -	03/2016	144(O) -	0/0
325	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR, MULTI STATE	04/2010	337.49 -	337.50	0.21	- -	-	-	0/0
326	BHADRACHALAM-KOVVUR - [N22000264]SCR, MULTI STATE	04/2012	923.23 -	923.23	1.01	- -	-	-	0/0
327	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR, ODISHA	03/2013	858.67 -	837.33	1.15	- -	-	-	0/0
328	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL	04/2011	289.64 -	760.00	0.09	- -	-	-	0/0
329	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	619.34 619.34	2,820.25	199.31	04/2014 03/2015	03/2018	47(O) 36(R)	0/0
330	BHANUPALI-BILASPUER BERI NL - [N22000273]NR, HIMACHAL PRADESH	04/2008	1,046.88 -	2,966.99	40.80	- -	-	-	0/0
331	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR, GUJARAT	04/2006	117.36 196.95	196.95	198.83	03/2011 -	-	-	0/0
332	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER, UTTAR PRADESH	03/2008	195.64 -	195.64	94.11	- -	-	-	0/0
333	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, MADHYA PRADESH	09/2007	687.20 -	800.00	793.71	03/2010 -	12/2015	69(O) -	0/0
334	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR, GUJARAT	04/2008	318.24 -	321.62	2.91	03/2012 -	-	-	0/0
335	BIHTA-AURANGABAD (NL) - [N22000170]ECOR, BIHAR	04/2008	326.20 -	326.20	1.68	- -	-	-	0/0
336	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER, MULTI STATE	04/2011	175.80 -	175.80	1.46	- -	-	-	0/0
337	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	434.00	35.90	- -	-	-	0/0
338	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR, ASSAM	09/1997	1,500.00 1,000.00	4,996.19	3,410.06	04/2008 03/2014	06/2017	110(O) 39(R)	0/0
339	CALICUT-MANGALORE (DL) (SR) - [220100151]SR, MULTI STATE	02/1996	240.00 -	579.37	599.40	- -	02/2012	-	0/0
340	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER, ODISHA	04/2010	149.90 -	230.00	68.67	03/2015 -	12/2016	21(O) -	0/0

Sector Wise Details									
(November 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
341	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	328.14	0.31	-	-	-	0/0
342	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	337.96	61.36	-	-	-	0/0
343	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00 -	951.24	619.87	-	03/2015	-	0/0
344	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	222.95	112.40	-	-	-	0/0
345	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	520.00	462.69	-	-	-	0/0
346	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	1,200.00	2.07	-	-	-	0/0
347	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	494.92	4.22	-	-	-	0/0
348	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	378.56	111.87	-	-	-	0/0
349	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 663.67	1,101.16	194.91	-	03/2017	-	0/0
350	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	243.78	30.05	-	-	-	0/0
351	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	367.77	-	-	-	-	0/0
352	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	692.43	-	-	-	-	0/0
353	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	595.91	89.60	-	-	-	0/0
354	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	1,347.26	164.55	-	-	-	0/0
355	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	573.78	166.89	-	-	-	0/0
356	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 575.00	1,242.25	1,005.81	03/2007	03/2016	108(O)	0/0
357	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	556.64	268.56	-	-	-	0/0
358	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	829.00	-	-	-	-	0/0
359	CUTTACK - BARANG (LD) - [220100326]RVNL,ODISHA	04/1995	127.13 -	225.00	193.37	-	10/2014	-	0/0
360	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	1,640.04	187.84	-	-	-	0/0
361	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	533.38 -	533.38	114.38	12/2011	-	-	0/0
362	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	968.60	180.86	12/2012	-	-	0/0
363	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	583.00	144.66	12/2015	03/2016	3(O)	0/0

Sector Wise Details									
(November 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
364	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	339.00	204.83	-	-	-	0/0
365	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	296.44	4.55	-	-	-	0/0
366	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	205.00	5.21	-	-	-	0/0
367	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	410.08	297.58	-	-	-	0/0
368	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	234.71	137.01	03/2015 -	03/2015	-	0/0
369	DELHI-SOHNANUHI-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	1,239.00	-	-	-	-	0/0
370	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	336.91	144.25	-	-	-	0/0
371	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	607.09	561.14	12/2012 12/2012	-	-	0/0
372	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	376.59	4.58	-	-	-	0/0
373	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 2,030.50	2,030.50	3.61	02/2019 -	02/2019	0(O) -	0/0
374	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 651.17	1,009.00	7.50	-	12/2019	-	0/0
375	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	4,487.70	-	-	03/2020	-	0/0
376	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	914.98	846.18	-	03/2016	-	0/0
377	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	4,874.58	1,911.65	03/2016 -	06/2018	27(O) -	0/0
378	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	275.08	141.55	03/2012 12/2013	03/2016	48(O) 27(R)	0/0
379	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	189.24	1.52	-	-	-	0/0
380	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	603.22	1.64	-	-	-	0/0
381	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 245.39	245.39	249.33	12/2008 -	10/2015	-	0/0
382	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	495.74	315.66	06/2013 06/2013	06/2013	-	0/0
383	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	654.00	-	-	-	-	0/0
384	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	1,922.00	1.89	-	-	-	0/0
385	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	270.00	301.84	02/2011 02/2011	-	-	0/0
386	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	415.67	14.00	-	-	-	0/0

Sector Wise Details									
(November 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
387	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	445.25	1.14	- -	-	-	0/0
388	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	197.73	-	- -	-	-	0/0
389	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	611.03 -	611.03	140.48	12/2011 11/2013	11/2013	-	0/0
390	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	261.70 -	280.00	195.94	02/2006 -	-	-	0/0
391	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,157.54	1,544.40	590.26	03/1998 -	12/2019	261(O) -	0/0
392	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	156.65	53.00	- -	-	-	0/0
393	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	283.54	0.31	- -	-	-	0/0
394	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	844.00	798.87	- 05/2009	03/2015	-	0/0
395	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	608.02	602.10	03/1994 -	03/2015	-	0/0
396	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	179.32	75.76	- -	-	-	0/0
397	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 3,845.60	3,845.60	2.33	02/2020 -	02/2020	0(O) -	0/0
398	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	157.17	76.90	- -	-	-	0/0
399	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	720.00 -	720.00	-	- -	-	-	0/0
400	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	367.17	17.19	- -	-	-	0/0
401	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	324.66	227.03	- -	-	-	0/0
402	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	267.09	1.50	- -	-	-	0/0
403	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	172.03	5.86	- -	-	-	0/0
404	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	1,185.64	442.82	- 09/2009	-	-	0/0
405	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	329.97	2.38	- -	-	-	0/0
406	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 -	1,289.92	1,092.98	- -	-	-	0/0
407	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	230.03	172.58	- -	-	-	0/0
408	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	829.74	96.76	03/2015 -	03/2015	-	0/0
409	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	400.00	-	- -	-	-	0/0
410	HOSADURGA - CHICKAJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA	04/2010	203.40 -	203.40	153.29	- -	09/2015	-	0/0
411	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	2,127.00	325.00	- -	-	-	0/0
412	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 -	1,618.00	-	- -	-	-	0/0

Sector Wise Details

(November 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
413	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	157.94	43.34	- -	-	-	0/0
414	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 393.46	1,026.00	181.48	03/2007 03/2007	03/2015	-	0/0
415	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	166.89	0.02	- -	-	-	0/0
416	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,900.00 -	1,900.00	-	- -	-	-	0/0
417	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	2,135.00	117.24	- -	-	-	0/0
418	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	313.24	230.62	01/1999 -	-	-	0/0
419	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	653.55	258.78	03/2014 -	-	-	0/0
420	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	162.96	143.62	- -	-	-	0/0
421	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	847.75	835.14	06/2007 -	-	-	0/0
422	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 501.69	1,043.56	819.19	03/2012 -	-	-	0/0
423	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	470.00	40.00	- -	-	-	0/0
424	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	230.00	218.67	- -	-	-	0/0
425	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	740.00	639.77	03/2012 03/2012	12/2012	-	0/0
426	JIRIBAM TO IMPHAL (TUPUI)(NL),(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 727.56	6,570.75	2,787.99	03/2011 03/2014	03/2019	96(O) 60(R)	0/0
427	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	2,050.00	194.45	- -	-	-	0/0
428	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	923.52	208.10	- -	-	-	0/0
429	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	174.56	63.08	- -	-	-	0/0
430	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	279.70	4.73	- -	-	-	0/0
431	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,062.36	1,651.54	1,621.40	- -	03/2018	-	0/0
432	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	643.00	-	- -	-	-	0/0
433	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	744.71 -	744.71	576.86	- -	03/2016	-	1/1
434	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	800.00	800.70	- -	-	-	0/0

Sector Wise Details									
(November 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
435	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM	04/1998	227.90 200.00	331.40	182.22	12/2012 -	03/2016	39(O) -	0/0
436	KATI HAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	1,727.27	743.74	12/2010 -	03/2018	87(O) -	0/0
437	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]JER,MULTI STATE	04/2010	423.66 -	423.66	163.59	03/2017 -	03/2017	0(O) -	0/0
438	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 -	1,054.35	8.06	- -	-	-	0/0
439	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	541.00	158.58	- -	-	-	0/0
440	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	276.00	305.29	03/2009 03/2009	-	-	0/0
441	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	1,995.25	355.02	- -	-	-	0/0
442	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 -	1,143.60	189.12	- -	03/2018	-	0/0
443	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	282.92 282.92	565.13	2.80	- 03/2014	03/2018	- 48(R)	0/0
444	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87 -	768.87	682.31	- 03/2010	03/2010	-	0/0
445	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	2,957.21 -	2,957.21	1,966.90	07/2005 -	-	-	0/0
446	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	418.17	260.67	- -	-	-	0/0
447	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE	04/2013	723.00 -	723.00	-	- -	-	-	0/0
448	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	341.41	325.36	03/2012 -	-	-	0/0
449	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	1,047.00	1.29	- -	-	-	0/0
450	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	252.96	1.48	- -	-	-	0/0
451	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	192.56	0.38	- -	-	-	0/0
452	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	346.15	14.61	- -	-	-	0/0
453	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]JER,MULTI STATE	04/1987	406.99 -	406.99	141.55	- -	-	-	0/0
454	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	1,630.97	488.76	05/2008 -	-	-	0/0
455	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]JER,MULTI STATE	04/2009	257.42 -	257.42	67.97	03/2014 -	03/2014	-	0/0
456	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM	04/2012	246.07 246.07	364.06	0.30	- -	03/2019	-	0/0
457	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 -	5,500.00	4,734.45	03/2009 -	03/2016	84(O) -	0/0

Sector Wise Details									
(November 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
458	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	480.00	3.51	07/2008 -	07/2008	-	0/0
459	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	450.00	16.97	-	-	-	0/0
460	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	800.00	0.69	-	-	-	0/0
461	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	493.96	121.27	-	-	-	0/0
462	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	343.00	216.17	-	-	-	0/0
463	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	900.05	853.83	12/2011 12/2010	-	-	0/0
464	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	378.56 -	791.59	5.41	-	-	-	0/0
465	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 315.13	365.00	2.52	-	12/2017	-	0/0
466	MANSABHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	369.00	188.93	-	-	-	0/0
467	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]JECR,BIHAR	04/1996	332.92 332.92	477.88	498.37	03/2012 -	-	-	0/0
468	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	1,112.00	-	-	-	-	0/0
469	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	279.54	1.38	01/1999 -	-	-	0/0
470	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPIUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	855.16	557.82	-	-	-	0/0
471	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	1,383.45	457.88	-	-	-	0/0
472	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	377.44	7.50	-	-	-	0/0
473	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 -	1,830.00	-	-	-	-	0/0
474	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	439.88	0.78	-	-	-	0/0
475	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	800.00	0.83	01/1999 -	-	-	0/0
476	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	426.00	-	01/1999 -	-	-	0/0
477	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	250.93	0.14	-	-	-	0/0
478	MOTIHARI-SITAMARHI (NL) - [N22000174]JECR,BIHAR	04/2006	211.00 -	926.09	4.41	-	-	-	0/0
479	MUDKHED-PARBHANI - [N22000283]SCR,MAHARASHTRA	04/2011	390.60 -	390.60	4.69	-	-	-	0/0
480	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 6,821.29	7,986.04	2,443.62	03/2014 03/2019	03/2019	60(O) 0(R)	0/0

Sector Wise Details

(November 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
481	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 236.41	645.00	309.19	- -	03/2015	-	0/0
482	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	1,350.91	380.62	- -	-	-	0/0
483	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	165.82 165.82	435.58	0.56	- -	03/2018	-	0/0
484	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	281.30	0.58	- -	-	-	0/0
485	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	228.05	1.52	- -	-	-	0/0
486	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	1,313.48	5.13	- -	-	-	0/0
487	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	883.00	755.50	02/2009 -	03/2015	-	0/0
488	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	2,100.00	391.95	07/2012 -	-	-	0/0
489	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	620.57	-	- -	-	-	0/0
490	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]JER,MULTI STATE	04/2010	494.54 -	494.54	31.20	- -	-	-	0/0
491	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	300.00 300.00	827.73	53.52	- -	03/2019	-	0/0
492	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	200.00 200.00	496.24	213.72	- -	03/2017	-	0/0
493	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 171.00	679.57	40.41	- -	03/2018	-	0/0
494	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	4,083.02 -	5,307.90	7.79	- 03/2016	03/2020	- 48(R)	0/0
495	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 210.00	394.28	233.46	- -	03/2017	-	0/0
496	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL	04/2010	221.42 205.31	563.13	22.39	- -	03/2019	-	0/0
497	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	36.80 36.38	1,336.57	255.55	- -	03/2019	-	0/0
498	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 1,798.00	1,887.90	-	- -	03/2019	-	0/0
499	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR,WEST BENGAL	04/2011	209.77 190.39	441.45	85.78	- -	03/2018	-	0/0
500	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR,WEST BENGAL	04/2012	283.55 278.21	288.81	11.74	- -	03/2018	-	0/0
501	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NFR,MULTI STATE	04/1999	523.17 380.60	1,653.55	1,040.11	- -	03/2018	-	0/0
502	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00 -	2,973.42	10.44	03/2015 03/2020	03/2020	60(O) 0(R)	0/0
503	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	733.00 733.00	2,531.34	1,732.43	12/2008 -	03/2018	111(O) -	0/0

Sector Wise Details

(November 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
504	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,069.60	35.40	03/2014 -	-	-	0/0
505	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINAY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	2,619.02	545.87	03/2016 -	03/2016	0(0) -	0/0
506	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	204.56	03/2016 -	06/2016	3(0) -	0/0
507	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	3,951.98	664.51	03/2016 -	03/2016	0(0) -	0/0
508	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, ANDHRA PRADESH	07/2006	743.00 -	1,117.11	562.07	03/2008 06/2008	-	-	0/0
509	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR, GUJARAT	04/2013	1,266.89 -	1,266.89	-	-	-	-	0/0
510	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	293.74 -	293.74	140.08	12/2010 -	-	-	0/0
511	PANVEL PEN DOUBLING - [N22000255]CR, MULTI STATE	04/2006	96.16 -	260.16	240.21	-	01/2015	-	0/0
512	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR, BIHAR	04/2001	624.47 -	2,921.00	2,521.72	10/2007 12/2012	12/2015	98(0) 36(R)	0/0
513	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, TELANGANA	12/1994	124.43 -	925.30	712.02	-	02/2014	-	0/0
514	PEN ROHA DOUBLING - [N22000254]CR, MULTI STATE	04/2007	98.74 -	203.00	227.84	-	03/2015	-	0/0
515	PHULERA - DIGANA DOUBLING - [N22000326]NWR, MULTI STATE	05/2015	600.00 -	600.00	-	-	-	-	0/0
516	PIRPAINTI-BHAGALPUR - [N22000222]ER, MULTI STATE	04/2011	261.38 -	261.38	21.21	-	-	-	0/0
517	PIRPAINTI-JASIDIH - [N22000219]ER, MULTI STATE	04/2013	915.98 -	915.98	0.09	-	-	-	0/0
518	PLASSEY-JAGANJ DOUBLING - [N22000220]ER, MULTI STATE	04/2011	248.07 -	248.07	29.10	03/2015 -	03/2015	-	0/0
519	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER, MULTI STATE	04/2011	299.60 -	299.60	-	03/2017 -	03/2017	0(0) -	0/0
520	PUSHKAR-MERTA - [N22000151]NWR, RAJASTHAN	04/2013	323.00 -	323.00	-	-	-	-	0/0
521	QADIAN-BEAS - [N22000295]NR, PUNJAB	04/2011	205.22 -	205.22	1.54	-	-	-	0/0
522	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR, TAMIL NADU	04/1999	460.94 -	1,030.00	-	01/1999 -	-	-	0/0
523	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR, MULTI STATE	03/1998	280.00 -	1,122.00	889.95	-	-	-	0/6
524	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL, ANDHRA PRADESH	04/2003	136.62 -	289.93	325.50	12/2007 03/2010	-	-	0/0
525	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR, BIHAR	04/2002	921.00 -	2,363.00	1,691.12	03/2009 12/2012	10/2015	-	0/0
526	RAJATGARH-BARANG(LD), ECR - [220100286]RVNL, ODISHA	04/1999	166.16 -	288.00	332.53	02/2009 02/2009	-	-	0/0

Sector Wise Details									
(November 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
527	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	209.00	2.64	12/2016 -	12/2016	0(O) -	0/0
528	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 913.48	913.48	457.67	- -	-	-	0/0
529	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	874.57	730.11	03/2013 -	09/2015	-	0/0
530	RAMGANJUMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	470.92 727.13	1,225.90	257.59	- -	03/2017	-	0/0
531	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	335.00	230.67	06/2004 -	12/2015	138(O) -	0/0
532	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	288.97	1.09	- -	-	-	0/0
533	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	872.22	794.11	- -	-	-	0/0
534	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	3,500.00	54.23	- -	-	-	0/0
535	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	1,421.25	420.33	03/2012 -	-	-	0/0
536	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	1,743.00	359.06	- -	-	-	0/0
537	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA	05/2015	400.00 -	400.00	-	- -	-	-	0/0
538	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	576.18	3.40	- -	-	-	0/0
539	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	714.10	65.93	04/2016 -	03/2017	11(O) -	0/0
540	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	193.44	53.01	- -	-	-	0/0
541	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	325.00	258.31	- -	-	-	0/0
542	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	355.81	294.07	- -	-	-	0/0
543	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	385.54	251.24	03/2010 -	-	-	0/0
544	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	380.00	-	- -	-	-	0/0
545	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	155.81	18.25	- -	12/2016	-	0/0
546	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 -	1,111.99	60.31	- -	-	-	0/0
547	SANTOSHUPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	268.52	78.81	- -	-	-	0/0
548	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 1,339.48	4,190.00	88.56	12/2015 -	03/2020	51(O) -	0/0
549	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	832.47	0.94	- -	-	-	0/0
550	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	239.32	17.17	- -	-	-	0/0

Sector Wise Details									
(November 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
551	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	297.47	51.82	- -	-	-	0/0
552	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	277.28	67.82	- -	-	-	0/0
553	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	466.65	-	- -	-	-	0/0
554	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	1,500.00	0.01	- -	-	-	0/0
555	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	818.29	153.92	02/2015 -	-	-	0/0
556	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	450.00	7.91	- -	-	-	0/0
557	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 732.06	516.23	597.72	03/2014 -	-	-	0/0
558	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	810.80	160.80	- -	-	-	0/0
559	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 1,013.74	1,428.00	466.36	06/2005 07/2011	12/2019	174(O) 101(R)	0/0
560	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	171.02 -	171.00	166.84	06/2013 -	01/2015	-	0/0
561	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	365.17	1.35	- -	-	-	0/0
562	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	1,188.91	687.63	- 12/2009	-	-	0/0
563	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR,TAMIL NADU	04/2011	190.10 -	190.10	33.19	- -	-	-	0/0
564	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	262.00	0.41	- -	-	-	0/0
565	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 -	1,080.00	194.61	- -	-	-	0/0
566	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 -	490.00	67.57	- -	-	-	0/0
567	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	167.73	124.14	03/2012 -	-	-	0/0
568	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 -	980.00	596.66	- -	-	-	0/0
569	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL	03/2000	1,049.69 3,385.14	3,404.92	3,551.53	12/2006 -	-	-	0/0
570	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	167.50	0.32	- -	-	-	0/0
571	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	1,801.01	1.47	- -	-	-	0/0
572	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	19,565.00	10,658.34	11/2002 -	12/2018	193(O) -	0/0
573	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	1,389.62	1,055.80	03/2014 -	-	-	0/0

Sector Wise Details									
(November 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
574	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	380.00	1.38	- -	-	-	0/0
575	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 -	1,564.54	420.71	03/2010 03/2017	03/2017	84(O) 0(R)	0/0
576	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	138.86	- -	-	-	0/0
577	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	1,280.83	1,031.83	- -	-	-	0/0
578	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 -	548.01	201.26	- 03/2010	-	-	0/0
579	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	685.17	206.59	- -	-	-	0/0
580	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	279.40	249.02	- -	-	-	0/0
581	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	2,501.05	84.11	- -	-	-	0/0
582	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	297.85	7.17	- -	-	-	0/0
583	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	348.85	0.34	- -	-	-	0/0
584	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	876.00	-	- -	-	-	0/0
585	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	860.43	-	- -	-	-	0/0
	Total		171,881.41 -	296,947.84	90,798.15				1/7
	ROAD TRANSPORT AND HIGHWAYS **								
586	REHABILITATION AND UPGRADE OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD,TELANGANA	01/2014	340.00 -	340.00	-	03/2016 -	03/2016	0(O) -	0/0
587	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	303.40	08/2013 -	-	-	0/0
588	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH	10/2012	250.50 -	250.50	-	10/2014 -	-	-	0/0
589	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	373.47	28.51	07/2014 -	-	-	0/0
590	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	351.54	-	05/2013 -	-	-	0/0
591	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	-	11/2013 -	-	-	0/0
592	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	624.00	333.72	04/2014 -	-	-	0/0
593	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	356.40	-	07/2014 -	-	-	0/0
594	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI,RAJASTHAN	03/2014	240.10 -	240.10	-	03/2016 -	03/2016	0(O) -	0/0
595	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR - [N24000238]NHAI,RAJASTHAN	01/2014	158.04 -	158.04	-	12/2015 -	12/2015	0(O) -	0/0

Sector Wise Details

(November 2015)

Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
596	2-LANING WITH PS OF JHALAWAR-RAJASTHAN-MP. BORDER - [N24000237]NHAI,RAJASTHAN	01/2014	177.32 -	177.32	86.65	01/2016 -	01/2016	0(0) -	0/0
597	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	52.86	01/2014 -	-	-	0/0
598	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	226.00	-	02/2014 -	-	-	0/0
599	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	664.00	-	02/2014 -	-	-	0/0
600	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	124.40	04/2014 -	-	-	0/0
601	2LANING WITH PS GOPALGANJ-CHAPRA - [N24000190]NHAI,BIHAR	12/2011	325.00 -	325.00	-	05/2014 -	-	-	0/0
602	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236]NHAI,RAJASTHAN	10/2013	677.79 -	677.79	59.09	04/2016 -	04/2016	0(0) -	0/0
603	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT	03/2012	828.00 -	828.00	52.01	09/2014 -	-	-	0/3
604	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	-	08/2014 -	-	-	0/0
605	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT	12/2010	1,008.50 -	1,008.50	1,151.00	06/2013 -	-	-	0/3
606	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	38.30	09/2013 -	-	-	0/0
607	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,GUJARAT	03/2011	785.50 -	785.50	745.80	08/2013 -	-	-	0/3
608	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	1,266.60	-	09/2016 -	09/2016	0(0) -	0/0
609	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	398.00	-	02/2014 -	-	-	0/0
610	4-LANING OF BRAHAMPURE-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	998.79	805.50	08/2013 -	-	-	0/0
611	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	1,078.84	967.10	08/2013 -	-	-	0/0
612	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	580.43	218.50	08/2013 -	-	-	0/0
613	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA	10/2013	283.25 -	283.25	-	10/2015 -	10/2015	-	0/0
614	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	-	07/2013 -	-	-	0/0
615	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	1,396.18	636.20	09/2014 -	-	-	0/0
616	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	348.16	269.40	09/2007 -	-	-	0/0
617	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	2,125.24	30.08	12/2015 -	12/2015	0(0) -	0/3
618	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA	02/2010	390.56 -	390.56	-	02/2012 -	-	-	0/0
619	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	291.00	09/2013 -	-	-	0/0
620	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	867.00	429.10	02/2015 -	-	-	0/0

Sector Wise Details									
(November 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
621	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	2,388.00	956.70	06/2014 -	-	-	0/0
622	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,KARNATAKA	12/2010	480.00 -	480.00	438.00	-	-	-	2/2
623	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	209.00	-	01/2013 -	-	-	0/0
624	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	500.29	450.90	08/2013 -	-	-	0/0
625	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	237.80	-	06/2008 -	-	-	0/0
626	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	195.00	-	06/2008 -	-	-	0/0
627	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	230.00	-	06/2005 -	-	-	0/0
628	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	309.56	258.40	04/2010 02/2016	02/2016	70(O) 0(R)	0/0
629	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	281.31	-	02/2010 -	-	-	0/0
630	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	790.90	03/2013 -	-	-	0/0
631	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	353.37	395.10	10/2011 -	-	-	0/0
632	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	572.30	761.40	10/2011 -	-	-	0/0
633	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA	03/2015	280.16 -	280.16	-	-	-	-	0/0
634	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD TO FO - [N24000258]DORTH,GOA	03/2015	184.05 -	184.05	-	-	-	-	0/0
635	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA	01/2014	267.16 352.00	352.05	2.79	11/2017 -	11/2017	0(O) -	0/0
636	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA	01/2014	255.75 348.00	348.43	13.79	09/2017 -	09/2017	0(O) -	0/0
637	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD,TELANGANA	03/2011	218.31 -	339.82	-	12/2015 -	12/2015	0(O) -	0/0
638	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA	03/2015	168.30 -	168.30	-	-	10/2017	-	0/0
639	CONSTRUCTION OF MAJOR/MINOR BRIDGE & ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO 45 - [N24000253]NHDP,MAHARASHTRA	08/2014	187.79 -	187.79	-	07/2016 -	07/2016	0(O) -	0/0
640	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA	03/2015	298.33 -	298.33	-	-	-	-	0/0
641	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	957.80	05/2013 -	-	-	0/0

Sector Wise Details									
(November 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
642	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	300.00	-	10/2008 -	-	-	0/0
643	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	1,928.22	255.30	04/2015 -	-	-	0/0
644	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	-	05/2010 -	-	-	0/0
645	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	593.00	485.70	07/2013 -	-	-	0/0
646	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	75.85	06/2013 -	-	-	0/0
647	DEVIHALLI-HASSAN - [N24000152]NHAI,KARNATAKA	12/2010	453.00 -	453.00	487.90	- -	-	-	1/1
648	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	200.00	-	06/2008 -	-	-	0/0
649	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	197.60	05/2008 12/2015	12/2015	91(O) 0(R)	0/0
650	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	232.45	-	09/2010 -	-	-	0/0
651	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA	03/2015	153.21 -	153.21	-	01/2017 -	01/2017	0(O) -	0/0
652	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	1,573.00	13.39	09/2015 -	-	-	0/0
653	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	332.94	-	09/2008 -	-	-	0/0
654	FOUR LANNING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	1,916.79	-	11/2016 -	11/2016	0(O) -	0/0
655	FOUR LANNING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00 -	1,232.00	87.61	08/2015 -	-	-	0/0
656	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDEAPAR BRIDGE - [N24000251]NHDP,GOA	03/2015	297.00 -	297.00	-	- -	10/2017	- -	0/0
657	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	682.00	34.81	10/2013 -	-	-	0/0
658	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	201.66	-	09/2008 -	-	-	0/0
659	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	1,141.00	1,200.00	08/2013 -	-	-	0/0
660	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	1,509.10	1,675.00	09/2012 -	-	-	2/3
661	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	198.16	-	04/2008 12/2015	12/2015	92(O) 0(R)	0/0
662	GUWAHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	175.96	182.50	04/2008 12/2015	12/2015	92(O) 0(R)	0/0
663	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	495.40	12/2009 -	-	-	0/0
664	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	361.00	-	02/2009 -	-	-	0/0

Sector Wise Details									
(November 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
665	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, ASSAM	12/2003	196.00 -	331.23	-	07/2009 -	-	-	0/0
666	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061]NHAI, ASSAM	12/2003	212.00 -	212.00	-	09/2007 -	-	-	0/0
667	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N240000212]NHAI, UTTARAKHAND	11/2011	478.00 -	478.00	245.20	10/2013 -	-	-	0/0
668	HAZARIBAGH-RANCHI - [N24000141]NHAI, JHARKHAND	08/2010	625.07 -	625.07	-	01/2013 -	-	-	0/0
669	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI, KARNATAKA	09/2010	946.00 -	946.00	-	- -	-	-	3/3
670	INDORE-DEWAS(NH-3) - [N24000159]NHAI, MADHYA PRADESH	11/2010	325.00 -	325.00	447.50	05/2013 -	-	-	0/0
671	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI, MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	-	-	0/0
672	JAIPUR-REENGUS - [N24000198]NHAI, RAJASTHAN	08/2010	267.81 -	267.81	564.50	02/2013 -	-	-	0/0
673	JAIPUR-TONK-DEOLI - [N24000135]NHAI, RAJASTHAN	06/2010	792.06 -	792.06	1,649.00	12/2012 -	-	-	0/0
674	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	-	07/2013 -	-	-	0/0
675	JORBAT - BARAPANI - [N24000180]NHAI, MEGHALAYA	01/2011	536.00 -	536.00	450.50	01/2014 -	-	-	0/0
676	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT	01/2011	953.88 -	953.88	560.10	07/2013 -	-	-	0/0
677	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI, RAJASTHAN	11/2009	795.00 -	795.00	1,056.00	05/2012 -	-	-	0/0
678	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI, RAJASTHAN	12/2003	275.00 -	250.39	-	10/2008 -	-	-	0/0
679	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL	02/2012	702.16 -	702.16	398.20	07/2014 -	-	-	0/0
680	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI, KARNATAKA	09/2010	671.00 -	671.00	-	- -	-	-	2/3
681	LUCKNOW-RAIBAREILI - [N24000207]NHAI, UTTAR PRADESH	07/1999	635.90 -	635.90	-	07/2012 -	-	-	0/0
682	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, ASSAM	12/2003	155.04 -	280.13	-	11/2008 -	-	-	0/0
683	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, ASSAM	12/2003	199.81 -	385.13	-	04/2009 -	-	-	0/0
684	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, ASSAM	12/2003	167.64 -	167.64	-	11/2008 -	-	-	0/0
685	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, ASSAM	12/2003	200.00 -	200.00	-	04/2009 -	-	-	0/0
686	MURADABAD-BAREILLY - [N24000154]NHAI, UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	1,313.00	06/2013 -	-	-	0/0
687	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, MULTI STATE	09/2011	754.00 -	754.00	511.00	03/2013 -	-	-	0/0
688	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, ASSAM	12/2003	264.72 -	264.72	-	06/2008 -	-	-	0/0
689	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI, MAHARASHTRA	04/2012	484.19 -	484.19	-	10/2014 -	-	-	0/0

Sector Wise Details									
(November 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
690	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	208.00	290.60	04/2008 01/2017	01/2017	105(O) 0(R)	0/0
691	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	258.40	06/2008 04/2016	04/2016	94(O) 0(R)	0/0
692	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	200.00	-	06/2008 -	-	-	0/0
693	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	2,159.00	-	06/2015 -	-	-	0/0
694	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	1,655.00	494.70	09/2013 -	-	-	0/0
695	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	557.00	932.30	02/2010 -	-	-	0/0
696	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	586.00	237.60	01/2014 -	-	-	0/0
697	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	153.70	09/2014 -	-	-	0/0
698	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	-	-	0/0
699	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00 -	807.00	-	10/2014 -	-	-	0/0
700	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	942.69	128.50	06/2014 -	-	-	0/0
701	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	574.00	536.00	03/2014 -	-	-	0/0
702	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	-	02/2013 -	-	-	0/0
703	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	940.00	1,293.00	07/2012 -	-	-	0/0
704	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,127.00	03/2013 -	-	-	0/0
705	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	835.00	122.70	01/2014 -	-	-	0/0
706	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	-	07/2015 -	-	-	0/0
707	RAJMARG CHORAH TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	251.03	-	10/2008 -	-	-	0/0
708	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,MULTI STATE	12/2012	1,479.00 -	1,479.00	162.70	06/2015 -	-	-	0/0
709	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN	03/2012	333.51 -	333.51	-	09/2014 -	-	-	0/0
710	REHABILITATION & UPGRADE OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]NHAI,MAHARASHTRA	12/2013	220.72 -	220.72	-	11/2016 -	11/2016	0(O) -	0/0
711	REHABILITATION & UPGRADE OF NH-222(61) FOM KM 284 TO 337 - [N24000250]NHAI,MAHARASHTRA	06/2014	260.39 -	260.39	-	11/2016 -	11/2016	0(O) -	0/0
712	REHABILITATION & UPGRADE OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHAI,MAHARASHTRA	01/2014	446.77 -	446.77	-	- -	06/2017	- -	0/0

Sector Wise Details									
(November 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
713	REHABILITATION & UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) T - [N24000267]PWD,ANDHRA PRADESH	02/2014	258.99 -	258.99	64.65	07/2014 -	07/2016	24(0) -	0/0
714	REHABILITATION & UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN T - [N24000265]PWD,ANDHRA PRADESH	11/2014	297.78 330.00	330.00	15.47	02/2017 -	02/2017	0(0) -	0/0
715	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH	12/2014	201.12 201.00	201.12	14.71	02/2015 -	02/2015	-	0/0
716	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH	03/2015	175.03 -	175.03	-	- -	-	-	0/0
717	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTIO - [N24000242]PWD,TELANGANA	12/2013	158.65 -	158.65	-	03/2016 -	03/2016	0(0) -	0/3
718	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]PWD,TELANGANA	12/2013	177.18 -	177.18	-	03/2016 -	03/2016	0(0) -	0/3
719	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]PWD,TELANGANA	01/2014	270.00 -	270.00	-	03/2016 -	03/2016	0(0) -	0/0
720	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]PWD,ANDHRA PRADESH	02/2015	241.61 -	241.61	23.83	02/2017 -	02/2017	0(0) -	0/0
721	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD,TELANGANA	10/2014	295.47 -	313.27	-	02/2017 -	02/2017	0(0) -	0/0
722	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]PWD,TELANGANA	10/2014	244.30 -	244.30	-	12/2016 -	12/2016	0(0) -	0/0
723	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH	07/2014	251.55 -	251.55	-	02/2015 -	02/2017	24(0) -	0/0
724	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	650.00	-	11/2013 -	-	-	0/0
725	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	805.39	543.70	03/2013 -	-	-	0/0
726	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	909.00	844.10	05/2014 -	-	-	0/0
727	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 -	157.47	-	09/2007 -	-	-	0/0
728	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	225.00	-	07/2008 -	-	-	0/0
729	SIX LANNING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	1,047.00	201.60	06/2014 -	-	-	0/0
730	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	535.00	-	12/2013 -	-	-	0/0

Sector Wise Details									
(November 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
731	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	14.58	12/2013 -	-	-	0/0
732	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	823.00	05/2014 -	-	-	0/0
733	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	-	08/2012 -	-	-	0/0
734	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	245.00	491.20	03/2008 04/2016	04/2016	97(O) 0(R)	0/0
735	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	-	06/2014 -	-	-	0/0
736	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	1,693.75	-	08/2011 -	-	-	2/2
737	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	567.00	891.10	11/2013 -	-	-	0/0
738	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	-	10/2013 -	-	-	0/0
739	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	101.30	05/2013 -	-	-	0/0
740	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,KARNATAKA	11/2010	680.00 -	680.00	-	-	-	-	2/2
741	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	771.10	03/2014 -	-	-	0/0
742	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI,ANDHRA PRADESH	09/2013	606.00 -	606.00	-	-	-	-	0/0
743	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	193.45	-	11/2012 -	-	-	0/0
744	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	1,287.95	-	11/2015 -	11/2015	0(O) -	0/0
745	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239]NHAI,RAJASTHAN	01/2014	368.15 -	368.15	-	01/2016 -	01/2016	0(O) -	0/0
746	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	-	02/2014 -	-	-	0/0
747	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI,TELANGANA	04/2014	1,123.17 -	1,123.17	-	-	-	-	0/0
748	YAN TO NIRMAL SEREABILITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA	12/2013	244.08 -	244.08	-	03/2016 -	03/2016	0(O) -	0/0
	Total		106,445.00 -	108,621.05	38,176.70				14/34
	SHIPPING AND PORTS								
749	ACQUISITION OF TWO (2) NOS OF 317000 DWT VLCC'S FROM JIANGSU RONGSHENG HEAVY INDUSTRIES CO.LTD.,CHIN - [N25000064]SHIPP.,MAHARASHTRA	10/2010	994.82 -	402.24	427.54	11/2013 -	11/2013	-	0/0

Sector Wise Details									
(November 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
750	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 -	1,460.00	1,038.00	12/2010 -	09/2017	81(O) -	0/0
751	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 669.46	669.46	412.00	12/2010 -	01/2016	61(O) -	0/0
752	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	600.00	139.80	03/2006 -	12/2015	117(O) -	0/0
753	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 373.22	409.83	353.18	04/2009 03/2010	08/2016	88(O) 77(R)	0/0
754	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	2,427.40	837.90	10/2008 -	-	-	0/0
	Total		5,412.28 -	5,968.93	3,208.42				0/0
	TELECOMMUNICATIONS								
755	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	384.00	74.74	10/2010 08/2015	11/2015	61(O) 3(R)	0/0
756	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	13,334.00	-	07/2015 -	-	-	0/0
	Total		13,718.00 -	13,718.00	74.74				0/0
	URBAN DEVELOPMENT								
757	2000 BOYS HOSTEL,(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 171.86	171.86	8.64	03/2016 -	05/2016	2(O) -	0/6
758	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD,WEST BENGAL	01/2009	225.81 -	225.81	136.53	06/2012 12/2015	12/2015	42(O) 0(R)	0/0
759	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA	05/2006	6,395.00 -	11,609.00	-	06/2011 -	-	-	3/3
760	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA	02/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019	0(O) -	0/0
761	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CENTRA - [N28000089]CPWD,TAMIL NADU	12/2015	209.00 -	209.00	-	-	-	-	0/0
762	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 14,600.00	14,600.00	11,544.24	12/2015 -	08/2016	8(O) -	1/24
763	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	884.30	-	08/2014 -	01/2016	17(O) -	0/0
764	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	188.87	5.79	12/2014 -	12/2016	24(O) -	0/0
765	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB	02/2014	388.00 -	388.00	-	01/2015 -	01/2015	-	0/0
766	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85 -	261.85	150.77	05/2013 10/2015	06/2016	37(O) 8(R)	0/0

Sector Wise Details									
(November 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
767	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI	05/2012	405.01 -	405.01	-	12/2014 -	04/2016	16(O) -	0/0
768	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD,ODISHA	11/2012	238.43 -	238.43	-	02/2015 -	-	-	0/0
769	CONSTRUCTION OF MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB - [N28000070]CPWD,PUNJAB	08/2005	191.24 -	191.24	-	08/2007 -	-	-	0/0
770	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	165.23	-	10/2012 -	-	-	0/0
771	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 -	315.00	3.11	06/2015 -	-	-	0/0
772	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	18.65	09/2015 07/2016	12/2016	15(O) 5(R)	0/0
773	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH	06/2014	157.84 -	157.84	-	03/2017 -	03/2017	0(O) -	0/0
774	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	38,585.00	18,738.92	03/2016 -	12/2016	9(O) -	0/0
775	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA - [N28000078]CPWD,BIHAR	11/2006	2,727.89 -	2,727.89	-	03/2010 -	-	-	0/0
776	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	57.69	11/2014 -	03/2016	16(O) -	0/0
777	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	1,219.21	-	07/2017 -	07/2017	0(O) -	0/0
778	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	5,181.79	-	07/2017 -	07/2017	0(O) -	0/0
779	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI - [N28000064]CPWD,DELHI	01/2010	162.90 -	162.90	-	07/2012 -	-	-	0/0
780	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	12/2015	11(O) -	0/0
781	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	8,680.00	-	03/2018 -	03/2018	0(O) -	0/0
782	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 -	241.33	-	11/2014 -	-	-	0/0
783	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI	06/2012	4,264.00 -	4,264.00	759.17	11/2019 -	11/2019	0(O) -	0/7
784	REHABILITATION AND STRENGTHENING OF SEWEWAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI(IN ZONE 2 IN - [N28000082]JnNURM,ANDHRA PRADESH	08/2007	246.90 -	246.90	-	-	-	-	0/0
785	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]CPWD,BIHAR	02/2012	171.10 -	171.10	-	09/2014 -	-	-	0/0
786	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	332.72	58.72	09/2016 01/2017	01/2017	4(O) 0(R)	0/0

Sector Wise Details									
(November 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
787	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	205.00	-	03/2012 -	-	-	0/0
	Total		136,783.82 -	141,997.82	31,482.23				4/40
	Grand Total		1,020,904.25	1,232,092.39	485,200.10				1740/3670

* - Information in respect of Ministry of Railways is as on 01.01.2015. Ministry of Railways is not updating the information.

** - Out of 137 projects, the data / information of only 37 projects were submitted online by the NHAI for the month of November 2015. The data / information in respect of remaining projects is as per last reported data i.e. June 2015.

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus Original Cost.


Summary of projects in the Flash Report for the month of November, 2015

Project Implementation - Current Status:

Number of Projects in Previous Month	782
Number of Projects completed/dropped/frozen in Current Month	1
Number of Projects elevated to the status of Major project during the current month	2
Number of Projects Added in Current Month	4
Number of Projects in Current Month	787

Brief Analysis


Project Status with respect to Original Schedule: Out of 787 projects, 7 projects are ahead of schedule, 146 projects are on schedule 208 projects are delayed. 396 projects do not have fixed dates of commissioning. 30 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

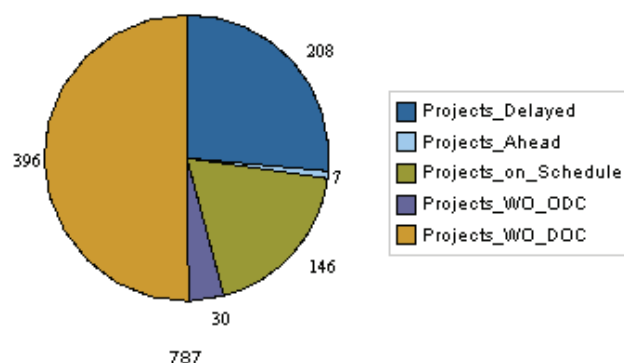

Investment Scenario

Total original cost of implementation of 787 projects when sanctioned, was of the order of Rs. 1020904.25 crore but this was subsequently revised to Rs. 1232092.39 crore implying a cost overrun of 20.7%. The expenditure incurred on these projects till November, 2015 is Rs. 485200.1 crore, which is 39.4% of the revised cost of the projects.

Figures are in Rs. Crore

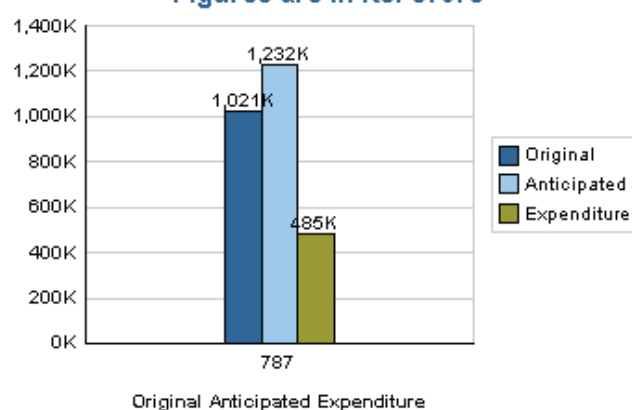

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	4


Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed.

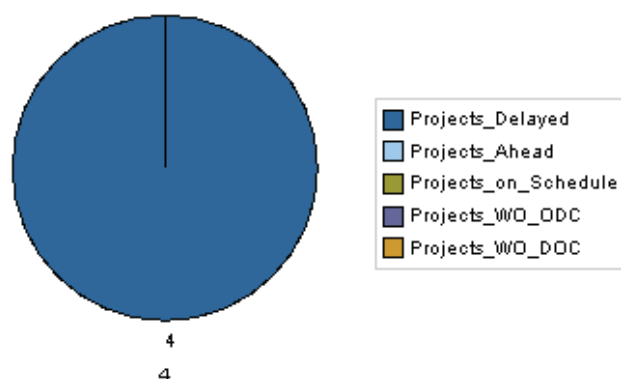

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 40442 crore but this was subsequently anticipated to Rs. 51918 crore implying a cost overrun of 28.4%. The expenditure incurred on these projects till November, 2015 is Rs. 33718 crore, which is 64.9% of the revised cost of the projects.

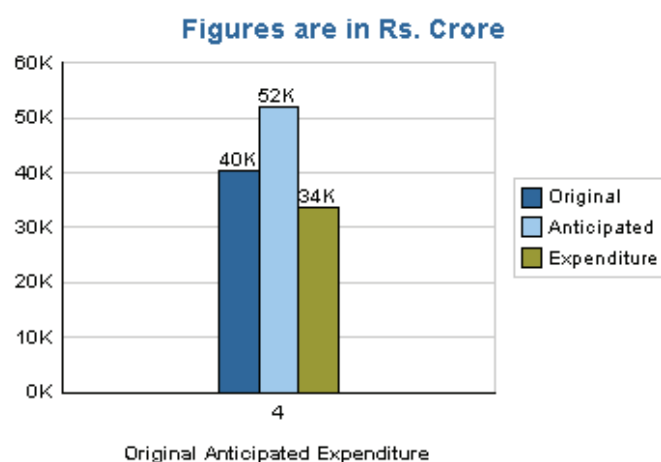

Sector wise current status of projects on the Flash Report


CIVIL AVIATION

Current Status:

Number of Projects	5
Number of Projects Delayed	1
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	3

Brief Analysis


Project Status with respect to Original Schedule: Out of 5 projects, 1 project is delayed. 3 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

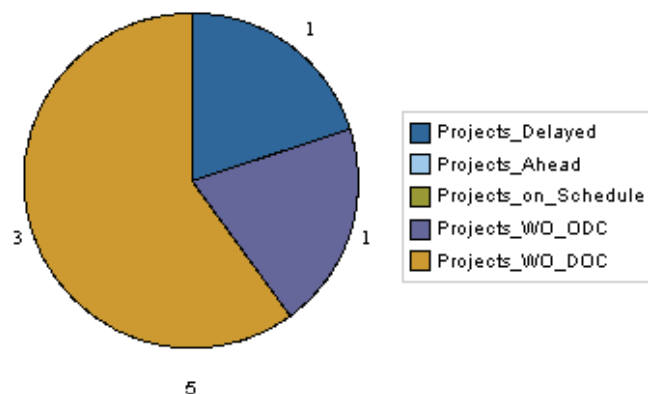

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 1521.56 crore but this was subsequently anticipated to Rs. 1530.45 crore implying a cost overrun of .6%. The expenditure incurred on these projects till November, 2015 is Rs. 839.1 crore, which is 54.8% of the revised cost of the projects.

Figures are in Rs. Crore

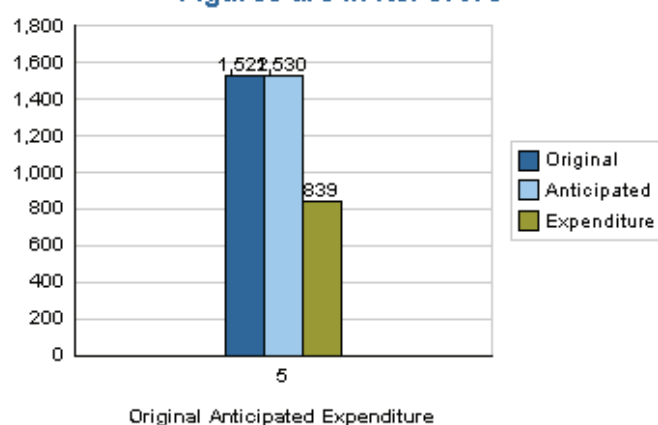

Sector wise current status of projects on the Flash Report


COAL

Current Status:

Number of Projects	81
Number of Projects On Schedule	36
Number of Projects Delayed	43
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	1

Brief Analysis


Project Status with respect to Original Schedule: Out of 81 projects, 1 project is ahead of schedule, 36 projects are on schedule 43 projects are delayed. 1 project does not have fixed dates of commissioning.

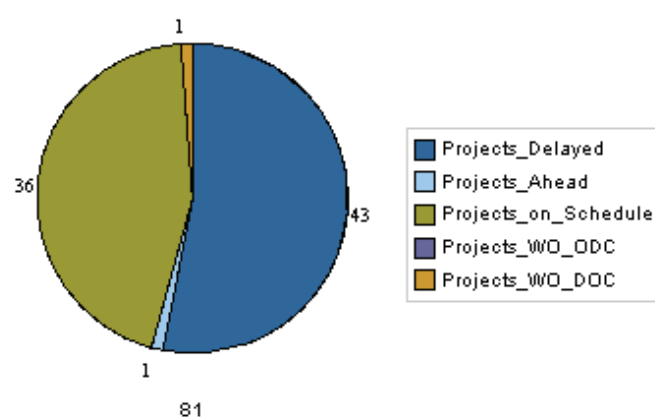

Investment Scenario

Total original cost of implementation of 81 projects when sanctioned, was of the order of Rs. 56886.73 crore but this was subsequently anticipated to Rs. 57765.87 crore implying a cost overrun of 1.5%. The expenditure incurred on these projects till November, 2015 is Rs. 14596.4 crore, which is 25.3% of the revised cost of the projects.

Figures are in Rs. Crore

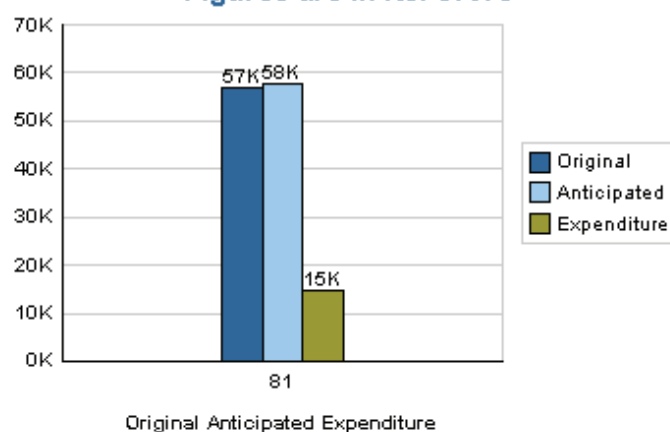

Sector wise current status of projects on the Flash Report

STEEL


Current Status:

Number of Projects	22
Number of Projects On Schedule	9
Number of Projects Delayed	10

Number of Projects Without Date Of Commissioning	3
--	---


Brief Analysis

Project Status with respect to Original Schedule: Out of 22 projects, 9 projects are on schedule 10 projects are delayed. 3 projects do not have fixed dates of commissioning.

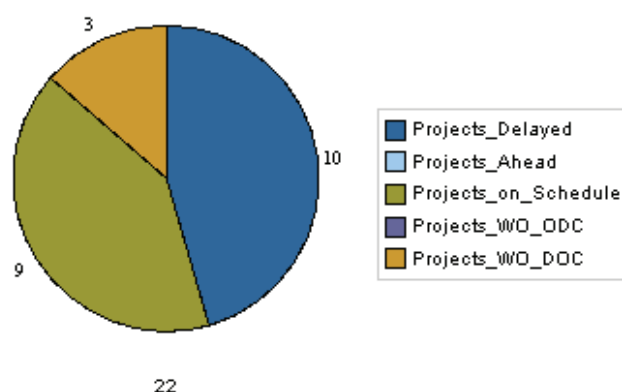

Investment Scenario

Total original cost of implementation of 22 projects when sanctioned, was of the order of Rs. 49833.99 crore but this was subsequently anticipated to Rs. 49979.39 crore implying a cost overrun of .3%. The expenditure incurred on these projects till November, 2015 is Rs. 26805.47 crore, which is 53.6% of the revised cost of the projects.

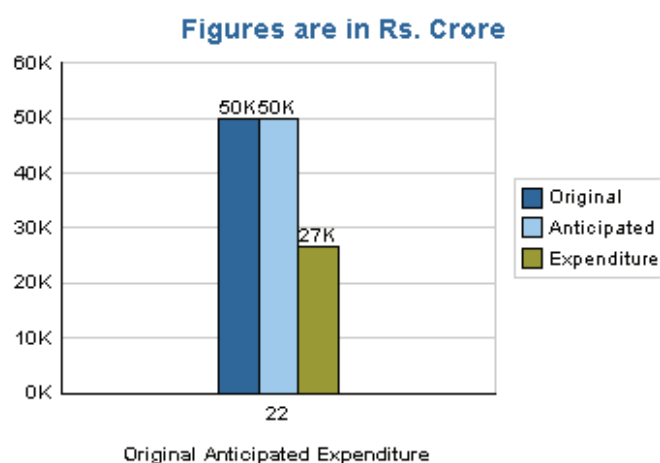

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	63
Number of Projects On Schedule	16
Number of Projects Delayed	37
Number of Projects Ahead	3
Number of Projects Without Date Of Commissioning	7


Brief Analysis

Project Status with respect to Original Schedule: Out of 63 projects, 3 projects are ahead of schedule, 16 projects are on schedule 37 projects are delayed. 7 projects do not have fixed dates of commissioning.

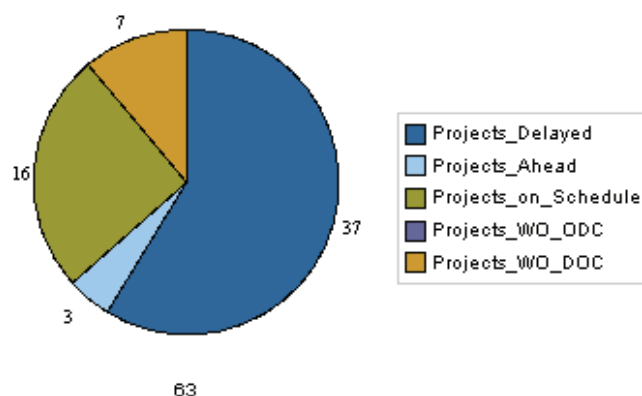

Investment Scenario

Total original cost of implementation of 63 projects when sanctioned, was of the order of Rs. 133205.31 crore but this was subsequently anticipated to Rs. 144838.01 crore implying a cost overrun of 8.7%. The expenditure incurred on these projects till November, 2015 is Rs. 67898.2 crore, which is 46.9% of the revised cost of the projects.

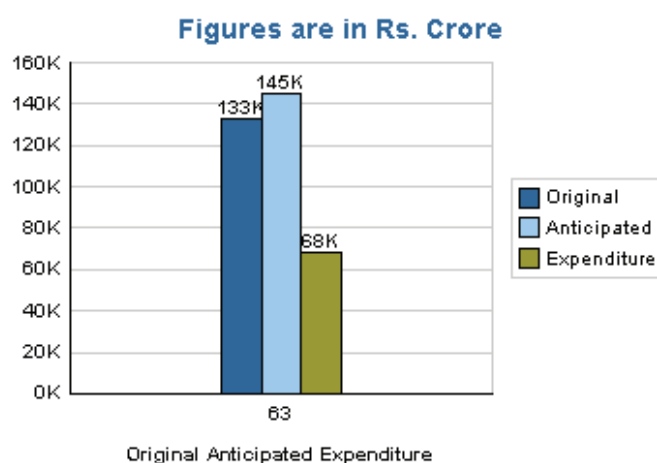

Sector wise current status of projects on the Flash Report


POWER

Current Status:

Number of Projects	105
Number of Projects On Schedule	42
Number of Projects Delayed	57
Number of Projects Ahead	3
Number of Projects Without Date Of Commissioning	3

Brief Analysis


Project Status with respect to Original Schedule: Out of 105 projects, 3 projects are ahead of schedule, 42 projects are on schedule 57 projects are delayed. 3 projects do not have fixed dates of commissioning.

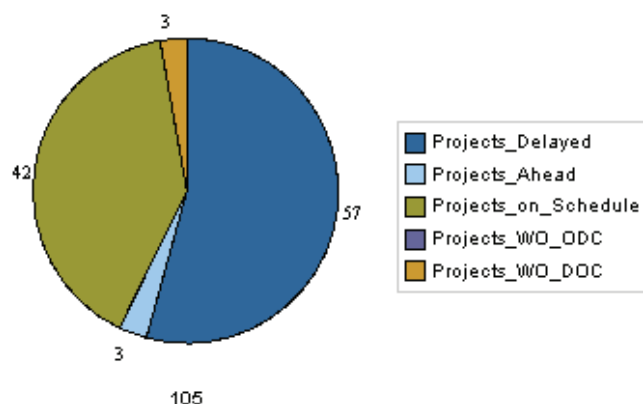

Investment Scenario

Total original cost of implementation of 105 projects when sanctioned, was of the order of Rs. 294151.17 crore but this was subsequently anticipated to Rs. 341570.36 crore implying a cost overrun of 16.1%. The expenditure incurred on these projects till November, 2015 is Rs. 167920.19 crore, which is 49.2% of the revised cost of the projects.

Figures are in Rs. Crore

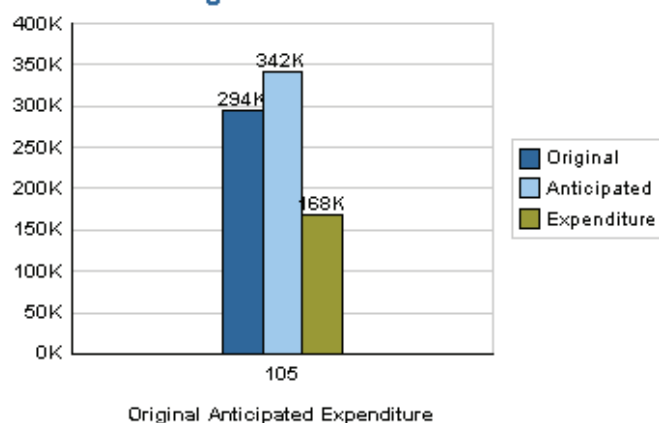

Sector wise current status of projects on the Flash Report


RAILWAYS

Current Status:

Number of Projects	296
Number of Projects On Schedule	8
Number of Projects Delayed	27
Number of Projects Without Original Date of Commissioning	26
Number of Projects Without Date Of Commissioning	235


Brief Analysis

Project Status with respect to Original Schedule: Out of 296 projects, 8 projects are on schedule 27 projects are delayed. 235 projects do not have fixed dates of commissioning. 26 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

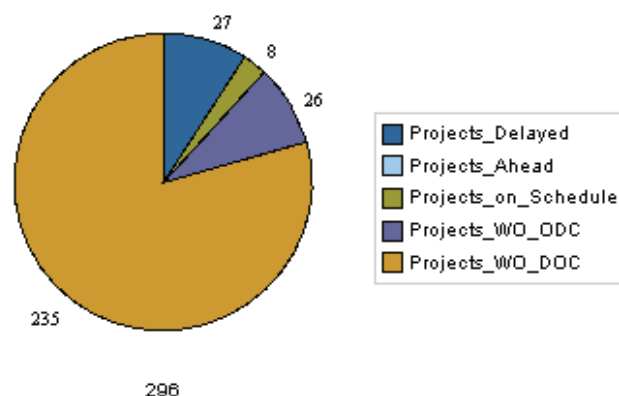

Investment Scenario

Total original cost of implementation of 296 projects when sanctioned, was of the order of Rs. 171881.41 crore but this was subsequently anticipated to Rs. 296947.84 crore implying a cost overrun of 72.8%. The expenditure incurred on these projects till November, 2015 is Rs. 90798.15 crore, which is 30.6% of the revised cost of the projects.

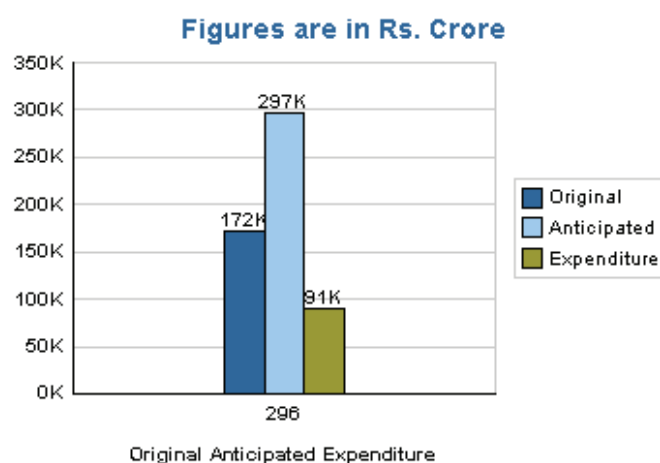

Sector wise current status of projects on the Flash Report


ROAD TRANSPORT AND HIGHWAYS

Current Status:

Number of Projects	163
Number of Projects On Schedule	25
Number of Projects Delayed	9
Number of Projects Without Original Date of Commissioning	3
Number of Projects Without Date Of Commissioning	126


Brief Analysis

Project Status with respect to Original Schedule: Out of 163 projects, 25 projects are on schedule 9 projects are delayed. 126 projects do not have fixed dates of commissioning. 3 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

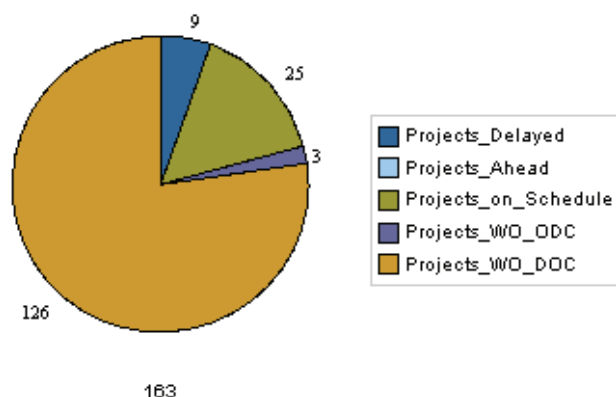

Investment Scenario

Total original cost of implementation of 163 projects when sanctioned, was of the order of Rs. 106445 crore but this was subsequently anticipated to Rs. 108621.05 crore implying a cost overrun of 2%. The expenditure incurred on these projects till November, 2015 is Rs. 38176.7 crore, which is 35.1% of the revised cost of the projects.

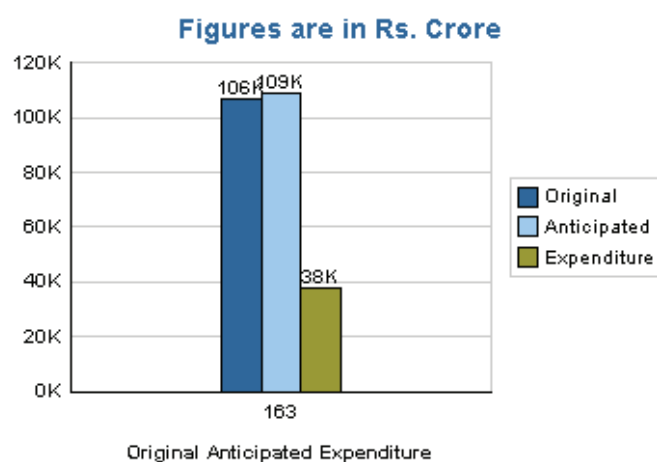

Sector wise current status of projects on the Flash Report


SHIPPING AND PORTS

Current Status:

Number of Projects	6
Number of Projects Delayed	4
Number of Projects Without Date Of Commissioning	2

Brief Analysis


Project Status with respect to Original Schedule: Out of 6 projects, 4 projects are delayed. 2 projects do not have fixed dates of commissioning.

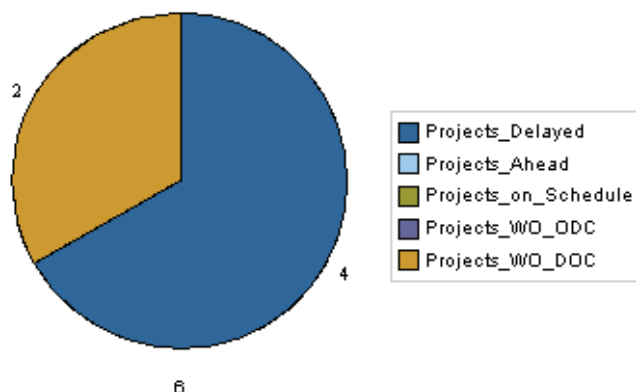

Investment Scenario

Total original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 5412.28 crore but this was subsequently anticipated to Rs. 5968.93 crore implying a cost overrun of 10.3%. The expenditure incurred on these projects till November, 2015 is Rs. 3208.42 crore, which is 53.8% of the revised cost of the projects.

Figures are in Rs. Crore

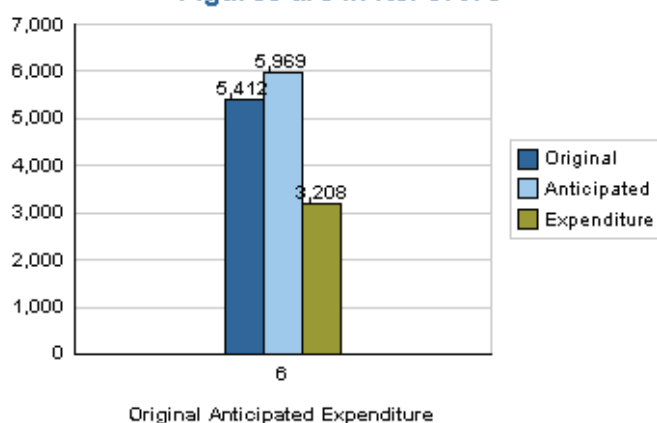

Sector wise current status of projects on the Flash Report


TELECOMMUNICATIONS

Current Status:

Number of Projects	2
Number of Projects Delayed	1
Number of Projects Without Date Of Commissioning	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 1 project is delayed. 1 project does not have fixed dates of commissioning.

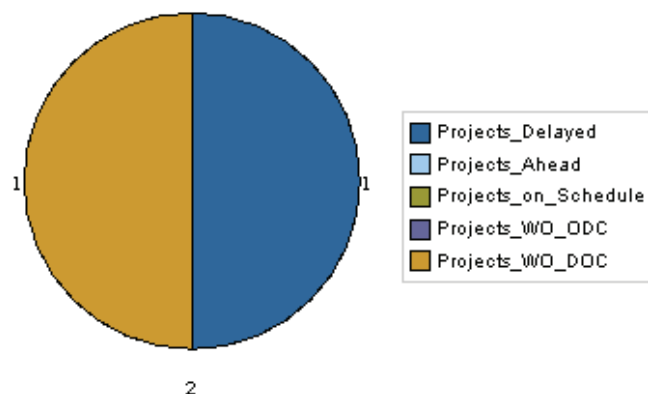

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 13718 crore but this was subsequently anticipated to Rs. 13718 crore. The expenditure incurred on these projects till November, 2015 is Rs. 74.74 crore, which is .5% of the revised cost of the projects.

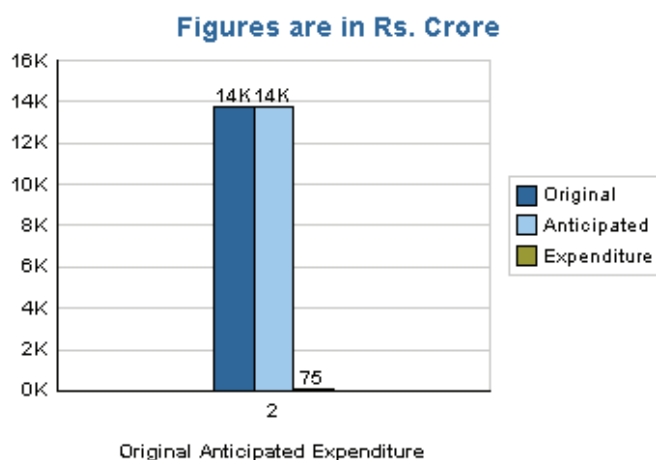

Sector wise current status of projects on the Flash Report

URBAN DEVELOPMENT


Current Status:

Number of Projects	31
Number of Projects On Schedule	6
Number of Projects Delayed	12

Number of Projects Without Date Of Commissioning	13
--	----


Brief Analysis

Project Status with respect to Original Schedule: Out of 31 projects, 6 projects are on schedule 12 projects are delayed. 13 projects do not have fixed dates of commissioning.

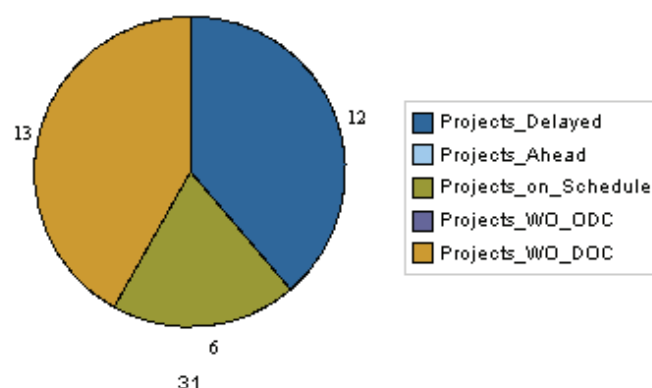

Investment Scenario

Total original cost of implementation of 31 projects when sanctioned, was of the order of Rs. 136783.82 crore but this was subsequently anticipated to Rs. 141997.82 crore implying a cost overrun of 3.8%. The expenditure incurred on these projects till November, 2015 is Rs. 31482.23 crore, which is 22.2% of the revised cost of the projects.

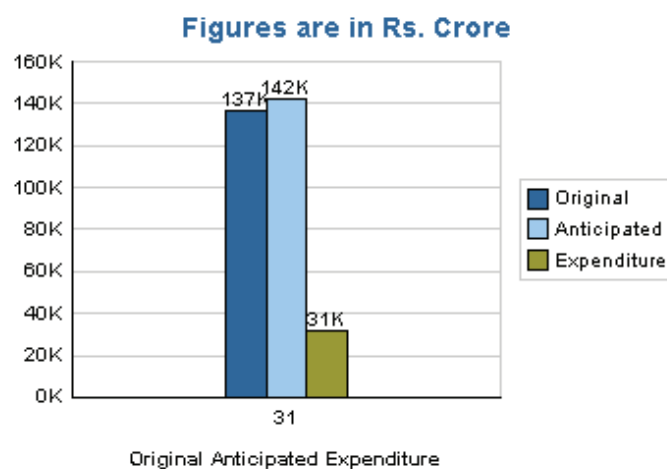

ANNEXURE

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE

(All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	ANDAMAN & NICOBAR ISLANDS	1	314.61	314.61	18.02
2	ANDHRA PRADESH	31	16,552.09	18,701.39	5,636.71
3	ARUNACHAL PRADESH	3	9,356.22	26,027.72	13,197.57
4	ASSAM	35	22,431.1	38,134.44	27,464.38
5	BIHAR	48	50,822.31	64,600.51	33,207.32
6	CHHATISGARH	29	81,307.1	82,969.27	47,136.71
7	D & N HAVELI	1	6,086.08	6,086.08	586.87
8	DELHI	14	49,464.96	49,464.96	20,139.62
9	GOA	5	1,395.15	1,377.54	305.01
10	GUJARAT	25	28,672.83	29,670.47	15,409.56
11	HARYANA	9	4,659.81	6,630.43	4,109.17
12	HIMACHAL PRADESH	4	7,154.09	12,973.29	5,426.75
13	JAMMU AND KASHMIR	7	21,314.62	40,235.3	14,935.09
14	JHARKHAND	38	39,714.33	42,197.08	11,470.7
15	KARNATAKA	33	65,975.04	80,937.81	16,880.65
16	KERALA	15	24,980.58	29,455.73	12,174.82
17	MADHYA PRADESH	19	22,774.88	24,985.97	8,157.61
18	MAHARASHTRA	55	1,04,291.59	1,14,584.52	31,346.44
19	MANIPUR	1	727.56	6,570.75	2,787.99
20	MEGHALAYA	3	4,845.02	6,069.9	458.29
21	MIZORAM	2	988.06	4,201.96	1,109.52
22	MULTI STATE	178	1,87,105.66	2,15,056.29	68,726.23
23	NAGALAND	2	5,124	7,461.12	10.44
24	ODISHA	41	69,443.31	78,531.35	41,771.81
25	PUNJAB	4	1,180.5	1,153.46	190.47
26	RAJASTHAN	31	27,361.24	27,844.69	12,993.44
27	SIKKIM	2	1,648.94	4,499.46	493.37
28	TAMIL NADU	41	61,482.24	81,074.93	46,993.47
29	TELANGANA	31	11,908.91	14,872.86	2,459.02
30	TRIPURA	4	2,381.35	6,012.47	2,777.26
31	UTTAR PRADESH	30	36,002.28	38,782.69	12,975.98
32	UTTARAKHAND	6	9,351.89	11,651.71	5,272.31
33	WEST BENGAL	39	44,085.9	58,961.63	18,577.5
TOTAL		787	10,20,904.25	12,32,092.39	4,85,200.1

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
1	KUDANKULAM APP (NPCIL)	ATOMIC ENERGY	12/2001	13,171	17270	20,962
2	PARBATI HEP (4X200 MW) (NHPC) II	POWER	09/2002	3,919.59	-	5,328.26
3	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	POWER	09/2003	6,285.33	-	7,870.78
4	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	POWER	09/2005	1,061.38	-	1,923.42
5	VIRAMGAM-BHILDI (WR) ,GC	RAILWAYS	04/1990	155.66	-	201.26
6	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL (SCR)	RAILWAYS	12/1994	124.43	-	712.02
7	UDHAMPUR-SRINAGAR-BARAMULLA (NL) ,NR	RAILWAYS	03/1995	2,500	3000	10,658.34
8	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR (NL) ,NEFR	RAILWAYS	04/1983	36.8	36.38	255.55
9	CALICUT-MANGALORE (DL) (SR)	RAILWAYS	02/1996	240	-	599.4
10	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA (NL) ,SWR	RAILWAYS	02/1997	295	-	1,092.98
11	KARUR-SALEM (NL) ,SR	RAILWAYS	02/1997	155.55	-	800.7
12	NANDYAL-YERRAGUNTALA (NL) ,SCR	RAILWAYS	03/1996	155.74	164.36	755.5
13	KANPUR-KASGANJ-MATHURA (GC) ,NER	RAILWAYS	03/1997	677.97	1062.36	1,621.4
14	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	RAILWAYS	09/1997	1,500	1000	3,410.06

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
15	MUNEERABAD-MAHABOBNAGAR (NL) , SCR	RAILWAYS	04/1997	218.24	236.41	309.19
16	RANCHI-LOHARDAGA (GC) , SER	RAILWAYS	04/1997	194.07	-	230.67
17	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	RAILWAYS	09/1998	247.66	-	488.76
18	JAYANAGAR-DARBHANGA-NARKATIA GANJ (GC) , ECR	RAILWAYS	04/1997	501.69	501.69	819.19
19	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	RAILWAYS	04/1999	108	427.21	436.85
20	KATIHAR - JOGBANI (GC) (NEFR)	RAILWAYS	09/2001	492.98	-	743.74
21	GULBARGA-BIDAR, SCR (NL)	RAILWAYS	02/1998	242.42	369.7	798.87
22	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD) , NR	RAILWAYS	03/2002	625.3	408.76	835.14
23	TIRUCHIRAPPALI-NAGORE-KARAIKKAL (SR) (GC)	RAILWAYS	09/1995	100	-	596.66
24	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR (SR) (GC)	RAILWAYS	03/1998	280	-	889.95
25	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) , NEFR	RAILWAYS	04/2000	733	733	1,732.43
26	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT (MTP)	RAILWAYS	03/2000	1,049.69	3385.14	3,551.53
27	GADWAL - RAICHUR (NL) , SCR	RAILWAYS	04/1998	92.63	-	301.84
28	JIND-SONEPAT (NL) , NR	RAILWAYS	01/2004	238.56	-	639.77

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
29	HARIDASPUR-PARADEEP (NL)	RAILWAYS	04/1996	301.64	-	442.82
30	RAJATGARH-BARANG (LD) , ECR	RAILWAYS	04/1999	166.16	-	332.53
31	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	RAILWAYS	04/2003	727.56	727.56	2,787.99
32	KOSI BRIDGE (NL) , ECR	RAILWAYS	04/2002	322.95	-	325.36
33	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL) , ECR	RAILWAYS	04/2002	921	-	1,691.12
34	PATNA GANGA BRIDGE (NL) , ECR	RAILWAYS	04/2001	624.47	-	2,521.72
35	ETAWAH-MAINPURI (NL) , NCR	RAILWAYS	04/1997	120	245.39	249.33
36	CUTTACK - BARANG (LD)	RAILWAYS	04/1995	127.13	-	193.37
37	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RAILWAYS	04/2000	133.41	207	305.29
38	RAICHUR-GUNTAKAL (DL) (SCR)	RAILWAYS	04/2003	136.62	-	325.5
39	CONSTRUCTION OF NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT	CIVIL AVIATION	01/2009	309.46	-	404.81
40	ASSAM GAS CRACKER PROJECT	PETROCHEMICALS	04/2006	5,460.61	8920	9,025.14
41	MARKETING TERMINAL AT PARADEEP	PETROLEUM	07/2009	199.75	-	205.75
42	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1)	PETROLEUM	10/2013	429.06	429	439.02

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
43	MARKETING TOP AT KORBA	PETROLEUM	01/2011	141.86	-	159.09
44	KISHANGANGA HEP (3X110 MW)	POWER	01/2009	3,642.04	-	4,276.75
45	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	POWER	02/2010	2,144	-	2,219.3
46	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH	POWER	11/2011	2,127.51	-	2,287.68
47	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	RAILWAYS	04/1996	332.92	332.92	498.37
48	BHOPAL BINA 3D LINE DOUBLING	RAILWAYS	09/2007	687.2	-	793.71
49	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	RAILWAYS	09/2007	404.19	-	457.88
50	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	RAILWAYS	09/2006	343.17	-	846.18
51	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	RAILWAYS	12/2006	170	-	417.7
52	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	RAILWAYS	09/2006	200	200	213.72
53	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	RAILWAYS	04/2006	325	-	420.71
54	AGARTALA SABROOM, NL, NEFR	RAILWAYS	04/2008	813.34	813.34	823.83
55	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	RAILWAYS	04/2007	482	-	730.11
56	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	RAILWAYS	04/1999	207.52	-	223.44

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
57	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	RAILWAYS	04/2006	117.36	196.95	198.83
58	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	RAILWAYS	04/1996	1,676.31	-	4,734.45
59	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR	RAILWAYS	04/2013	456	-	557.82
60	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	RAILWAYS	04/2010	739.65	-	794.11
61	SAKRI-HASANPUR ROAD (NL)	RAILWAYS	04/1999	175.69	-	258.31
62	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	RAILWAYS	04/1999	198.68	-	268.56
63	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	RAILWAYS	04/1998	271.24	-	462.69
64	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	RAILWAYS	04/2008	822.39	-	1,031.83
65	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	RAILWAYS	04/1999	895	575	1,005.81
66	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIE	RAILWAYS	04/2007	247	-	619.87
67	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI	RAILWAYS	04/1999	523.17	380.6	1,040.11
68	PEN ROHA DOUBLING	RAILWAYS	04/2007	98.74	-	227.84
69	PANVEL PEN DOUBLING	RAILWAYS	04/2006	96.16	-	240.21
70	MUNIRABAD (GINGERA) -RAICHUR NL	RAILWAYS	04/2007	179.65	-	380.62

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
71	JHARSUGUDA-RENGALI DOUBLING	RAILWAYS	03/2006	201	-	218.67
72	GUWHATI TO NALBARI (AS-4)	ROAD TRANSPORT AND HIGHWAYS	12/2003	175.96	-	182.5
73	SONAPUR TO GUWAHTI (AS-3)	ROAD TRANSPORT AND HIGHWAYS	12/2003	245	-	491.2
74	NALBARI TO BIJNI (AS-6)	ROAD TRANSPORT AND HIGHWAYS	12/2003	225	-	258.4
75	NALBARI T BIJNI (AS-7)	ROAD TRANSPORT AND HIGHWAYS	12/2003	208	230	290.6
76	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	ROAD TRANSPORT AND HIGHWAYS	12/2003	160	-	197.6
77	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	ROAD TRANSPORT AND HIGHWAYS	03/2005	557	-	932.3
78	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	ROAD TRANSPORT AND HIGHWAYS	03/2005	940	-	1,293
79	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	ROAD TRANSPORT AND HIGHWAYS	03/2010	1,509.1	-	1,675
80	KISHANGARH-AJMER-BEAWER	ROAD TRANSPORT AND HIGHWAYS	11/2009	795	-	1,056
81	CHENNAI-TADA (SIX LANE)	ROAD TRANSPORT AND HIGHWAYS	04/2009	353.37	-	395.1
82	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15)	ROAD TRANSPORT AND HIGHWAYS	05/2009	572.3	-	761.4
83	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM)	ROAD TRANSPORT AND HIGHWAYS	05/2009	1,108	-	3,466
84	JAIPUR-TONK-DEOLI	ROAD TRANSPORT AND HIGHWAYS	06/2010	792.06	-	1,649

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
85	TALEGAON-AMRAVATI	ROAD TRANSPORT AND HIGHWAYS	11/2009	567	-	891.1
86	DEVIHALLI-HASSAN	ROAD TRANSPORT AND HIGHWAYS	12/2010	453	-	487.9
87	MURADABAD-BAREILY	ROAD TRANSPORT AND HIGHWAYS	04/2010	1,267	-	1,313
88	INDORE-DEWAS (NH-3)	ROAD TRANSPORT AND HIGHWAYS	11/2010	325	-	447.5
89	4 LANNING OF AHMEDABAD TO GODHARA	ROAD TRANSPORT AND HIGHWAYS	12/2010	1,008.5	-	1,151
90	GHAZIABAD-ALIGARH NH-91	ROAD TRANSPORT AND HIGHWAYS	02/2011	1,141	-	1,200
91	JAIPUR-REENGUS	ROAD TRANSPORT AND HIGHWAYS	08/2010	267.81	-	564.5

Details of Projects Ahead of Schedule w.r.t. Original Schedule

(November 2015)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>POWER</u>						
1	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]	2/2014	243.53 -	243.53	185.63	08/2016 -	12/2015
2	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203]	2/2015	302.49 -	302.49	147.75	02/2016 -	12/2015
	Total		546.02 -	546.02	333.38		
	<u>COAL</u>						
3	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	3.52	03/2021 -	03/2017
	Total		555.52 -	555.52	3.52		
	<u>POWER</u>						
4	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]	8/2014	188.75 -	188.75	70.77	02/2017 -	03/2016
	Total		188.75 -	188.75	70.77		
	<u>PETROLEUM</u>						
5	MARKETING TOP AT KORBA - [N16000186]	1/2011	141.86 -	232.00	159.09	09/2016 -	03/2016
6	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]	7/2014	419.04 -	419.04	240.86	01/2017 -	06/2016
7	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]	11/2014	6,068.80 -	6,068.80	523.70	04/2019 -	03/2019
	Total		6,629.70 -	6,719.84	923.65		
	Grand Total		7,919.99	8,010.13	1,331.32		

Details of On Schedule Projects w.r.t. Original Schedule

							(November 2015)
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
1	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
2	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	5/2015	397.09 -	397.09	-	03/2019 -	03/2019
3	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]	5/2014	479.15 -	479.15	10.25	03/2019 -	03/2019
4	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]	12/2009	510.85 -	510.85	224.44	03/2016 -	03/2016
5	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.10 -	490.10	203.58	03/2017 -	03/2017
6	RAMPUR BATURA OCP (4.0 MTY) - [N06000049]	8/2015	1,186.64 -	1,186.64	1.33	03/2023 -	03/2023
7	ADASA UG TO OC - [N06000133]	8/2015	288.90 -	288.90	-	03/2023 -	03/2023
8	GOKUL - [N06000120]	11/2014	267.67 -	267.67	176.11	03/2018 -	03/2018
9	AMERA OC RCE - [N06000123]	2/2015	335.97 -	335.97	30.90	03/2018 -	03/2018
10	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	295.56	79.02	03/2019 -	03/2019
11	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	127.86	03/2020 -	03/2020
12	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	486.27	93.51	03/2016 -	03/2016
13	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	783.81	03/2023 03/2023	03/2023
14	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	5.43	03/2023 03/2023	03/2023
15	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]	5/2014	337.66 -	337.66	0.29	03/2019 -	03/2019
16	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	28.78	03/2021 -	03/2021
17	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	620.40	03/2026 -	03/2026
18	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	76.43	03/2020 -	03/2020
19	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	31.57	03/2021 -	03/2021
20	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	116.97	03/2020 -	03/2020
21	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	15.85	03/2020 -	03/2020
22	KAPURIA UG(PSLW) - [N06000108]	8/2011	988.35 -	988.35	45.27	04/2017 -	04/2017

							(November 2015)
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
23	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	92.30	03/2021 -	03/2021
24	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]	8/2012	1,055.05 -	1,055.05	191.06	03/2018 -	03/2018
25	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	122.91	03/2016 -	03/2016
26	DURGAPUR OPENCASST PROJECT - [N06000136]	2/2015	916.24 -	916.24	-	03/2023 -	03/2023
27	KULDA EXPN OC. (5.00 MTY) - [N06000115]	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
28	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]	12/2009	1,352.04 -	1,143.54	808.39	03/2016 -	03/2016
29	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
30	KHADIA EXPANSION OPENCASST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	125.67	03/2018 -	03/2018
31	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	51.53	03/2025 -	03/2025
32	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.33	-	03/2022 -	03/2022
33	BHANEGAON OC - [N06000121]	2/2015	187.94 -	187.94	46.65	03/2023 -	03/2023
34	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	108.44	03/2021 -	03/2021
35	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	158.45	03/2021 -	03/2021
36	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	108.17	03/2020 -	03/2020
	Total		31,381.09 -	31,276.11	4,485.37		
	<u>FERTILISERS</u>						
37	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	197.79	37.66	11/2016 -	11/2016
	Total		197.79 -	197.79	37.66		
	<u>HEALTH AND FAMILY WELFARE</u>						
38	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT & OTHERS-EMERGENCY BLOCK - [N21000005]	11/2013	196.70 -	196.70	-	01/2016 -	01/2016
39	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS - SUPER SPECIALITY BLOCK - [N21000004]	9/2013	444.70 -	444.70	228.19	12/2015 -	12/2015
	Total		641.40 -	641.40	228.19		
	<u>MINES</u>						
40	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]	9/2011	1,856.00 -	1,856.00	-	09/2017 -	09/2017

							(November 2015)
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		1,856.00	1,856.00	.00		
	<u>PETROLEUM</u>						
41	REWARI KANPUR PIPELINE PROJECT - [N16000145]	2/2012	1,210.64	1,446.34	1,249.03	11/2015	11/2015
42	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06	714.25	59.42	10/2017	10/2017
43	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	3/2012	14,225.00	16,504.00	9,087.43	05/2016	05/2016
44	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]	2/2015	2,899.93	2,899.93	502.37	05/2017	05/2017
45	GAMJI REDEVELOPMENT PROJECT - [N16000202]	5/2015	1,671.22	1,881.22	-	11/2019	11/2019
46	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]	5/2015	257.87	257.87	33.94	11/2016	11/2016
47	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00	3,150.00	110.77	09/2017	09/2017
48	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]	8/2015	2,818.88	2,818.88	-	03/2019	03/2019
49	TWENTY NOS. FEEDER GAS LINES - [N16000192]	3/2009	228.64	214.19	135.00	12/2016	12/2016
50	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]	3/2014	2,476.82	2,476.82	368.95	12/2018	12/2018
51	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	6/2014	5,706.47	5,813.25	2,268.83	05/2017	05/2017
52	PARADIP LPG IMPORT FACILITY - [N16000196]	1/2015	690.00	690.00	15.00	07/2018	07/2018
53	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	7/2011	352.56	450.55	10.60	03/2017	03/2017
54	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]	3/2014	238.50	238.50	1.07	03/2017	03/2017
55	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]	2/2014	163.88	163.88	46.91	07/2016	07/2016
56	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]	9/2011	202.25	160.16	68.96	07/2016	07/2016
	Total		36,899.72	39,879.84	13,958.28		
	<u>POWER</u>						
57	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	7/2012	1,527.00	1,527.00	142.00	08/2017	08/2017
58	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44	12,532.44	2,151.00	08/2018	08/2018
59	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]	7/2013	3,363.12	3,363.12	882.00	12/2016	12/2016
60	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	1/2013	12,964.60	12,964.60	4,609.32	01/2018	01/2018

							(November 2015)
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
61	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	1/2015	203.28 -	203.28	18.38	07/2017 -	07/2017
62	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]	5/2015	780.33 -	780.33	-	07/2017 -	07/2017
63	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]	5/2015	436.68 -	436.68	398.45	12/2016 -	12/2016
64	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]	8/2014	288.49 -	288.49	48.40	02/2017 -	02/2017
65	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]	9/2013	680.69 -	680.69	421.64	03/2016 -	03/2016
66	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58 -	14,366.58	2,241.00	02/2019 -	02/2019
67	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]	5/2014	829.98 -	829.98	64.00	08/2016 -	08/2016
68	MOUDA STPP STAGE 2 - [N18000132]	3/2012	7,921.47 -	7,921.47	4,704.00	09/2016 -	09/2016
69	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]	12/2014	6,517.36 -	6,517.36	231.99	04/2018 -	04/2018
70	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME - PART B - [N18000196]	4/2015	3,705.61 -	3,705.61	138.53	04/2018 -	04/2018
71	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]	4/2015	1,479.30 -	1,479.30	60.62	04/2017 -	04/2017
72	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]	3/2015	1,394.52 -	1,394.52	-	05/2017 -	05/2017
73	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]	3/2015	1,071.24 -	1,071.24	-	09/2017 -	09/2017
74	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]	3/2014	155.57 -	155.57	1.00	03/2016 -	03/2016
75	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 -	522.29	47.20	11/2016 -	11/2016
76	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]	9/2013	1,575.30 -	1,575.30	623.05	05/2016 -	05/2016
77	WARDHA-HYDERABAD 765 KV LINK - [N18000183]	1/2015	3,662.02 -	3,662.02	295.06	05/2018 -	05/2018
78	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	2/2014	908.08 -	908.08	114.91	06/2016 -	06/2016
79	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]	3/2015	550.06 -	550.06	1.60	03/2018 -	03/2018
80	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	891.00	03/2019 -	03/2019
81	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]	2/2014	378.71 -	378.71	113.06	10/2016 -	10/2016
82	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]	1/2015	268.80 -	268.80	20.32	03/2018 -	03/2018
83	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	11,638.55	4,480.00	09/2017 -	09/2017
84	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.84	149.00	09/2019 -	09/2019

(November 2015)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
85	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]	5/2014	303.07 -	303.07	19.70	07/2016 -	07/2016
86	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]	2/2014	539.82 -	539.82	100.76	06/2016 -	06/2016
87	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]	1/2015	871.62 -	871.62	1.90	10/2017 -	10/2017
88	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]	6/2014	400.47 -	400.47	45.19	04/2017 -	04/2017
89	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,364.52	430.87	04/2016 -	04/2016
90	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]	7/2015	2,247.37 -	2,247.37	15.10	07/2018 -	07/2018
91	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	11,846.00	5,137.00	06/2017 -	06/2017
92	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]	10/2014	8,112.12 -	8,112.12	-	04/2020 -	04/2020
93	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]	11/2014	972.42 -	972.42	-	11/2017 -	11/2017
94	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]	2/2014	167.40 -	167.40	84.40	12/2015 -	12/2015
95	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I) - [N18000198]	5/2015	312.94 -	312.94	2.11	05/2016 -	05/2016
96	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]	7/2015	307.18 -	307.18	0.80	11/2017 -	11/2017
97	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	702.99	03/2018 -	03/2018
98	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]	3/2015	197.40 -	197.40	-	03/2018 -	03/2018
	Total		133,086.59 -	133,086.59	29,388.35		
	<u>RAILWAYS</u>						
99	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANPUR & TANPUR-BANSI PAHARPUR - [N22000158]	4/2010	622.41 -	2,030.50	3.61	02/2019 -	02/2019
100	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	4/2010	423.66 -	423.66	163.59	03/2017 -	03/2017
101	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	4/2010	2,913.51 -	2,619.02	545.87	03/2016 -	03/2016
102	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	4/2012	632.68 -	816.55	48.00	03/2016 -	03/2016
103	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	1,176.09 -	3,845.60	2.33	02/2020 -	02/2020
104	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	4/2011	299.60 -	299.60	-	03/2017 -	03/2017

							(November 2015)
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
105	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	4/2010	3,951.98	3,951.98	664.51	03/2016	03/2016
106	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	4/2012	148.77	209.00	2.64	12/2016	12/2016
	Total		10,168.70	14,195.91	1,430.55		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
107	2-LANING WITH PS OF JHALAWAR-RAJASTHAN-MP. BORDER - [N24000237]	1/2014	177.32	177.32	86.65	01/2016	01/2016
108	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236]	10/2013	677.79	677.79	59.09	04/2016	04/2016
109	REHABILITATION & UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]	6/2014	260.39	260.39	-	11/2016	11/2016
110	REHABILITATION & UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN T - [N24000265]	11/2014	297.78 330.00	330.00	15.47	02/2017	02/2017
111	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]	11/2013	1,916.79	1,916.79	-	11/2016	11/2016
112	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24	2,125.24	30.08	12/2015	12/2015
113	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]	2/2015	241.61	241.61	23.83	02/2017	02/2017
114	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]	10/2014	244.30	244.30	-	12/2016	12/2016
115	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]	1/2014	270.00	270.00	-	03/2016	03/2016
116	CONSTRUCTION OF MAJOR/MINOR BRIDGE & ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO 45 - [N24000253]	8/2014	187.79	187.79	-	07/2016	07/2016
117	REHABILITATION & UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]	12/2013	220.72	220.72	-	11/2016	11/2016
118	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]	12/2013	177.18	177.18	-	03/2016	03/2016
119	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	1/2014	255.75 348.00	348.43	13.79	09/2017	09/2017
120	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR - [N24000238]	1/2014	158.04	158.04	-	12/2015	12/2015
121	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]	3/2015	153.21	153.21	-	01/2017	01/2017
122	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTIO - [N24000242]	12/2013	158.65	158.65	-	03/2016	03/2016

							(November 2015)
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
123	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]	1/2014	267.16 352.00	352.05	2.79	11/2017 -	11/2017
124	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]	3/2011	218.31 -	339.82	-	12/2015 -	12/2015
125	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]	10/2014	295.47 -	313.27	-	02/2017 -	02/2017
126	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	4/2014	1,266.60 -	1,266.60	-	09/2016 -	09/2016
127	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]	6/2013	1,287.95 -	1,287.95	-	11/2015 -	11/2015
128	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]	1/2014	340.00 -	340.00	-	03/2016 -	03/2016
129	YAN TO NIRMAL SEREHALITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]	12/2013	244.08 -	244.08	-	03/2016 -	03/2016
130	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239]	1/2014	368.15 -	368.15	-	01/2016 -	01/2016
131	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]	3/2014	240.10 -	240.10	-	03/2016 -	03/2016
	Total		12,050.38 -	12,399.48	231.70		
	<u>STEEL</u>						
132	REBUILDING OF COB-7 AT BSL - [N12000083]	10/2013	245.67 -	245.67	68.15	05/2016 -	05/2016
133	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]	5/2015	1,154.18 -	1,154.18	17.72	12/2017 -	12/2017
134	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	33.61	10/2016 -	10/2016
135	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]	3/2015	1,034.01 -	1,034.01	-	10/2017 -	10/2017
136	3RD CONVERTER AND 4TH CASTER - [N12000088]	7/2011	974.76 -	974.76	197.53	07/2016 -	07/2016
137	ALTERNATE GAS NETWORK AT BSL - [N12000093]	3/2015	255.19 -	255.19	22.05	03/2018 -	03/2018
138	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]	4/2015	3,127.30 -	3,127.30	156.76	04/2018 -	04/2018
139	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]	2/2014	4,749.00 -	4,749.00	1.29	09/2017 -	09/2017
140	TURBO BLOWER - 5 - [N12000092]	12/2009	280.00 -	280.00	15.77	09/2016 -	09/2016
	Total		12,163.11 -	12,308.51	512.88		
	<u>URBAN DEVELOPMENT</u>						

(November 2015)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
141	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]	2/2014	26,405.14 -	26,405.14 -	-	02/2019 -	02/2019
142	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]	6/2014	157.84 -	157.84 -	-	03/2017 -	03/2017
143	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,264.00 -	759.17	11/2019 -	11/2019
144	NAGPUR METRO RAIL - [N28000085]	8/2014	8,680.00 -	8,680.00 -	-	03/2018 -	03/2018
145	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,219.21 -	-	07/2017 -	07/2017
146	KOCHI METRO RAIL PROJECT - [N28000081]	7/2012	5,181.79 -	5,181.79 -	-	07/2017 -	07/2017
	Total		45,907.98 -	45,907.98 -	759.17		
	Grand Total		284,352.76	291,749.61	51,032.15		

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(November 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	09/2016	62.57
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	22,462.00	12/2008 -	06/2016	70.54
	Total		16,663.00 -	28,139.00			
	<u>CIVIL AVIATION</u>						
3	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]	10/2012	217.60 -	244.10	03/2015 -	09/2015	12.18
	Total		217.60 -	244.10			
	<u>COAL</u>						
4	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 -	486.57	03/2012 -	03/2017	87.58
5	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	03/2016 -	03/2016	31.87
6	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	03/2016	478.50
7	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	479.63	03/2013 -	03/2017	0.02
8	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	486.27	03/2016 -	03/2016	12.97
	Total		1,532.31 -	2,879.45			
	<u>HEAVY INDUSTRY</u>						
9	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78
	Total		1,718.00 -	3,827.30			
	<u>PETROCHEMICALS</u>						
10	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	9,965.00	04/2012 -	12/2015	82.49
	Total		5,460.61 -	9,965.00			

(November 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	PETROLEUM						
11	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]	12/2012	3,513.07 -	4,619.94	02/2016 -	12/2017	31.51
12	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	450.55	03/2017 -	03/2017	27.79
13	MARKETING TERMINAL AT PARADEEP - [N16000168]	07/2009	199.75 -	239.73	07/2013 -	11/2015	20.02
14	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	03/2016	70.49
15	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	10/2017 -	10/2017	17.66
16	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	05/2013	4,124.35 -	4,941.49	04/2016 -	12/2017	19.81
17	MARKETING TOP AT KORBA - [N16000186]	01/2011	141.86 -	232.00	09/2016 -	03/2016	63.54
18	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	06/2014	5,706.47 -	5,813.25	05/2017 -	05/2017	1.87
19	GAMJI REDEVELOPMENT PROJECT - [N16000202]	05/2015	1,671.22 -	1,881.22	11/2019 -	11/2019	12.57
20	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) [N16000128]	03/2011	861.79 -	1,256.72	05/2013 -	04/2016	45.83
21	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00 -	34,555.00	11/2012 -	01/2016	16.05
22	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	05/2016	29.42
23	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	03/2012	14,225.00 -	16,504.00	05/2016 -	05/2016	16.02
24	REWARI KANPUR PIPELINE PROJECT - [N16000145]	02/2012	1,210.64 -	1,446.34	11/2015 -	11/2015	19.47
25	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	02/2012	666.00 -	838.08	11/2015 -	11/2016	25.84
26	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79	10/2014 -	03/2017	49.38
27	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]	01/2006	732.00 -	1,227.00	10/2011 -	03/2016	67.62
28	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	08/2016	37.72
	Total		68,022.56 -	80,741.01			
	POWER						
29	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	7,818.68	09/2009 -	12/2018	99.48
30	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	18,063.89	09/2010 -	-	187.40
31	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]	09/2005	1,061.38 -	1,929.15	09/2009 -	06/2016	81.76

(November 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
32	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	721.81	09/2010 -	06/2016	51.10
33	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]	09/2010	2,074.86 -	2,348.37	03/2013 -	01/2016	13.18
34	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	13,762.80	08/2013 -	12/2017	23.65
35	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	12/2018	29.14
36	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	6,749.18	09/2011 -	03/2017	54.25
37	BOKARO THERMAL POWER STATION-A - [N18000199]	08/2006	2,313.00 4,139.00	4,237.67	12/2011 -	03/2016	83.21
38	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]	04/2007	4,122.00 8,781.00	9,606.82	02/2011 -	01/2017	133.06
39	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,476.34	12/2009 06/2016	12/2016	159.38
40	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	02/2016 -	09/2019	79.77
41	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	06/2014 -	-	31.17
42	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,487.49	08/2013 -	05/2016	159.15
43	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	346.79	08/2014 -	02/2016	16.63
44	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]	12/2011	1,746.65 -	2,228.71	08/2014 -	06/2016	27.60
45	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,497.72	01/2016 -	11/2016	50.95
46	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,159.07	11/2008 -	-	21.34
47	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	15,095.67	01/2011 -	05/2018	73.65
48	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	07/1998	368.72 -	1,381.71	07/2006 02/2015	10/2017	274.73
49	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	1,007.57	07/2013 -	12/2015	139.32
	Total		60,901.26 -	108,384.06			
	<u>RAILWAYS</u>						
50	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]	04/1986	158.77 274.56	608.02	03/1994 -	03/2015	282.96
51	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	36.80 274.41	1,336.57	- -	03/2019	3,531.98
52	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37	- -	02/2012	141.40
53	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 -	800.00	- -	-	414.30

(November 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
54	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	492.98	1,727.27	12/2010	03/2018	250.37
55	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	844.00	- 05/2009	03/2015	248.16
56	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263	03/1998	280.00	1,122.00	-	-	300.71
57	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	330.00	1,047.00	-	-	217.27
58	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69	3,404.92	12/2006	-	224.37
59	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63	270.00	02/2011	-	191.48
60	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90	2,371.85	03/2005 12/2008	12/2019	2,019.62
61	JIND-SONEPAT (NL),NR - [220100280	01/2004	238.56	740.00	03/2012	12/2012	210.19
62	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64	1,185.64	- 09/2009	-	293.06
63	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00	2,363.00	03/2009	10/2015	156.57
64	RAMGANJ-MUNDI-BHOPAL (NL),WCR - [220100314	04/2001	470.92 727.13	1,225.90	-	03/2017	160.32
65	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316	04/2003	218.19	343.00	-	-	57.20
66	ETAWAH-MAINPURI (NL),NCR - [220100318	04/1997	120.00	245.39	12/2008	10/2015	104.49
67	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79	1,101.16	-	03/2017	186.92
68	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23	818.29	02/2015	-	346.59
69	CUTTACK - BARANG (LD) - [220100326	04/1995	127.13	225.00	-	10/2014	76.98
70	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	276.00	03/2009 03/2009	-	106.88
71	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	810.78	810.80	-	-	0.00
72	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329	04/2003	136.62	289.93	12/2007 03/2010	-	112.22
73	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045	03/1997	261.70	280.00	02/2006	-	6.99
74	BHOPAL BINA 3D LINE DOUBLING - [N22000077	09/2007	687.20	800.00	03/2010	12/2015	16.41
75	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079	09/2007	404.19	1,383.45	-	-	242.28
76	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080	09/2006	343.17	914.98	-	03/2016	166.63

(November 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
77	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 -	490.00	- -	-	292.00
78	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	1,080.00	- -	-	136.84
79	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	03/2016	60.77
80	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,820.25	04/2014 -	03/2018	355.36
81	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	332.92 283.95	477.88	03/2012 -	-	43.54
82	VIRAMGAM-BHILDI(WR),GC - [220100062]	04/1990	155.66 -	548.01	- 03/2010	-	252.06
83	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56 -	791.59	- -	-	109.11
84	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 -	1,117.11	03/2008 06/2008	-	50.35
85	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	653.55	03/2014 -	-	0.06
86	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012 -	-	135.68
87	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]	04/2006	117.36 196.95	196.95	03/2011 -	-	67.82
88	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41
89	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	499.30 -	2,501.05	- -	-	400.91
90	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70 -	279.70	- -	-	0.72
91	PEN ROHA DOUBLING - [N22000254]	04/2007	98.74 -	203.00	- -	03/2015	105.59
92	PANVEL PEN DOUBLING - [N22000255]	04/2006	96.16 -	260.16	- -	01/2015	170.55
93	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26
94	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	-	651.97
95	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97
96	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]	04/2008	184.26 -	2,000.00	- -	-	985.42
97	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	576.18	- -	-	100.76
98	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99	- -	-	183.41
99	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	-	24.09
100	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	-	57.65

(November 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
101	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47 -	- -	- -	47.93
102	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,743.00 -	- -	- -	79.63
103	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85 -	- -	- -	2.29
104	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	337.50 -	- -	- -	0.00
105	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	329.97 -	- -	- -	50.10
106	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50 -	- -	- -	14.14
107	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00 -	- -	- -	72.07
108	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77 -	- -	- -	12.38
109	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]	04/1999	460.94 -	1,030.00 -	01/1999 -	- -	123.46
110	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	800.00 -	01/1999 -	- -	71.50
111	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00 -	01/1999 -	- -	53.96
112	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	514.68 -	2,820.00 -	- -	- -	447.91
113	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	1,781.98 -	03/2004 -	03/2016 -	259.68
114	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	09/1997	1,500.00 -	4,996.19 -	04/2008 12/2011	06/2017 -	233.08
115	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	1,630.97 -	05/2008 -	- -	558.55
116	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	04/1997	501.69 335.77	1,043.56 -	03/2012 -	- -	108.01
117	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72 -	12/2009 -	06/2015 -	300.67
118	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	541.00 -	- -	- -	232.17
119	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	2,531.34 -	12/2008 -	03/2018 -	245.34
120	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	470.21 -	1,995.25 -	- -	- -	324.33
121	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	6,570.75 -	03/2011 -	03/2019 -	803.12
122	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	322.95 -	341.41 -	03/2012 -	- -	5.72
123	PATNA GANGA BRIDGE (NL), ECR - [220100308]	04/2001	624.47 -	2,921.00 -	10/2007 -	12/2015 -	367.76
124	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	485.00 -	03/2011 -	- -	185.29

(November 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
125	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	496.24	- -	03/2017	148.12
126	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	300.00 -	827.73	- -	03/2019	175.91
127	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	850.00 -	2,973.42	03/2015 -	03/2020	249.81
128	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
129	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	5,500.00	03/2009 -	03/2016	228.10
130	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	2,876.00	03/2014 -	03/2018	253.60
131	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	565.13	- -	03/2018	99.75
132	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,190.00	12/2015 -	03/2020	212.81
133	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]	03/1997	677.97 1,062.36	1,651.54	- -	03/2018	143.60
134	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
135	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60
136	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	625.30 408.76	847.75	06/2007 -	-	35.57
137	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,564.54	03/2010 -	03/2017	381.40
138	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]	04/1995	304.00 -	968.60	12/2012 -	-	218.62
139	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 -	288.00	02/2009 02/2009	-	73.33
140	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	385.54	03/2010 -	-	18.66
141	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	155.74 164.36	883.00	02/2009 -	03/2015	466.97
142	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	218.24 236.41	645.00	- -	03/2015	195.55
143	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
144	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30 -	1,544.40	03/1998 -	12/2019	299.79
145	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	03/2015	160.76
146	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,428.00	06/2005 -	12/2019	385.76
147	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	194.07 -	335.00	06/2004 -	12/2015	72.62

(November 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
148	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	- -	-	840.53
149	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR [220100183	02/1997	295.00 -	1,289.92	- -	-	337.26
150	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	04/1996	138.00 -	1,382.78	- -	-	902.01
151	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107	04/2007	482.00 -	874.57	03/2013 -	09/2015	81.45
152	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	980.00	- -	-	880.00
153	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123	04/2008	318.24 -	321.62	03/2012 -	-	1.06
154	SAMBALPUR-TALCHER DOUBLING - [N22000315	03/2011	679.27 -	1,111.99	- -	-	63.70
155	JHARSUGUDA-RENGALI DOUBLING - [N22000317	03/2006	201.00 -	230.00	- -	-	14.43
156	KIRANDUL - JAGDALPUR DOUBLING - [N22000318	12/2012	826.57 -	1,143.60	- -	03/2018	38.35
157	DELANG-PURI DOUBLING - [N22000320	03/2011	165.16 -	234.71	03/2015 -	-	42.11
158	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321	04/2014	182.92 -	197.73	- -	-	8.10
159	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	04/2012	148.77 -	209.00	12/2016 -	12/2016	40.49
160	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	925.30	- -	02/2014	643.63
161	AMRAVATI-NARKHER NL(CR) - [220100118	06/1994	663.01 175.30	725.00	06/1999 -	07/2012	9.35
162	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	550.00 -	1,566.00	- -	-	184.73
163	CHHAPRA-BALLIA UP - [N22000134	03/2013	295.00 -	494.92	- -	-	67.77
164	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143	04/1994	320.66 -	913.48	- -	-	184.87
165	VIRAMGAM-SAMAKHIALI (DL) - [N22000145	04/2011	446.00 -	685.17	- -	-	53.63
166	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147	04/2011	2,082.75 -	3,500.00	- -	-	68.05
167	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	04/2011	1,176.09 -	3,845.60	02/2020 -	02/2020	226.98
168	THIYAT HAMIRA-SANU - [N22000149	04/2013	236.93 -	262.00	- -	-	10.58
169	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTURGARH-UDAIPUR [N22000152	04/2013	456.00 -	855.16	- -	-	87.54

(November 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
170	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	-	17.92
171	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	218.39	- -	-	2.34
172	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	02/2019	226.23
173	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00	- -	-	62.32
174	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00	- -	12/2019	82.25
175	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
176	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44
177	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	03/2016	88.40
178	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	12/2017	41.36
179	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
180	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
181	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	- -	-	338.91
182	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
183	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00 -	1,887.90	- -	03/2019	5.00
184	ATTIPPATTU-PUTTUR - [N22000184]	04/2008	446.87 -	528.00	- -	-	18.16
185	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,200.00	- -	-	129.22
186	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
187	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17
188	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]	04/1998	271.24 -	520.00	- -	-	91.71
189	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,280.83	- -	-	55.74
190	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
191	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	563.13	- -	03/2019	154.33
192	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,242.25	03/2007 -	03/2016	38.80

(November 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
193	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00 -	886.65	- -	03/2018	251.85
194	DIMAPUR-TIZIT NL - [N22000196]	04/2013	4,274.00 -	4,487.70	- -	03/2020	5.00
195	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77 -	441.45	- -	03/2018	110.44
196	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	288.81	- -	03/2018	1.86
197	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22	- -	-	109.04
198	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	-	173.71
199	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	247.00 -	951.24	- -	03/2015	285.12
200	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	222.95	- -	-	16.29
201	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02 -	5,307.90	- -	03/2020	30.00
202	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	679.57	- -	03/2018	180.56
203	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	03/2017	63.25
204	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	435.58	- -	03/2018	162.68
205	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]	04/1999	523.17 -	1,653.55	- -	03/2018	216.06
206	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12 -	453.10	- -	03/2018	45.17
207	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	364.06	- -	03/2019	47.95
208	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	03/2016	29.06
209	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	800.00	- -	-	33.02
	Total		81,685.74 -	208,168.14			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
210	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	-	28.93
211	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	-	92.75
212	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	-	80.68
213	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	-	68.99
214	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	-	106.50

(November 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
215	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	04/2010 -	02/2016	42.25
216	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00 -	201.66	09/2008 -	-	30.10
217	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	-	2.29
218	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]	10/2014	295.47 -	313.27	02/2017 -	02/2017	6.02
219	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]	03/2011	218.31 -	339.82	12/2015 -	12/2015	55.66
220	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	01/2014	255.75 348.00	348.43	09/2017 -	09/2017	36.24
221	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]	01/2014	267.16 352.00	352.05	11/2017 -	11/2017	31.78
222	REHABILITATION & UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN T - [N24000265]	11/2014	297.78 330.00	330.00	02/2017 -	02/2017	10.82
	Total		3,920.93 -	6,121.59			
	<u>SHIPPING AND PORTS</u>						
223	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016]	11/2007	1,228.00 -	1,460.00	12/2010 -	09/2017	18.89
224	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	03/2006 -	12/2015	300.00
225	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]	03/2007	245.67 -	409.83	04/2009 -	08/2016	66.82
226	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]	01/2007	366.39 -	669.46	12/2010 -	01/2016	82.72
	Total		1,990.06 -	3,139.29			
	<u>STEEL</u>						
227	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	10/2016 -	10/2016	42.39
	Total		343.00 -	488.40			
	<u>URBAN DEVELOPMENT</u>						
228	BANGALORE METRO RAIL PROJECT - [N28000008]	05/2006	6,395.00 -	11,609.00	06/2011 -	-	81.53
	Total		6,395.00 -	11,609.00			

(November 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	Grand Total		248,850.07	463,706.34			

Details of Delayed Projects w.r.t. Original and Revised Schedule

(November 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00 17,270.00	22,462.00	20,962.00	12/2008 10/2013	06/2016	90	70.54	Local protest/agitation, slippage of commitments
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVINI,TAMIL NADU	09/2003	3,492.00 -	5,677.00	-	09/2010 -	09/2016	72	62.57	NR
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	7,477.00	12/2015 10/2016	10/2017	22	0	Rescheduled due to late receipt of financial keeping
4	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	5,279.00	12/2016 04/2017	05/2018	17	0	Manufacturing is delayed
	Total		40,442.00 -	51,918.00	33,718.00					
	<u>CIVIL AVIATION</u>									
5	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	309.46	404.81	01/2011 06/2016	09/2017	80	0	Terminal Building work stopped by local residents demanding compensation citing damages to their properties.
	Total		309.46 -	309.46	404.81					
	<u>COAL</u>									
6	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	297.02	03/2010 -	03/2016	72	0	Coal Evacuation problem
7	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,920.50	03/2014 -	03/2016	24	0	i) Delay in procurement of major HEMM & construction of CHP & In-pit Conveyor transport system.
8	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,701.89	03/2014 -	03/2016	24	0	i) Delay in procurement of major HEMM & construction of CHP including Silo.
9	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,UTTAR PRADESH	06/2011	789.88 741.62	741.62	493.43	03/2013 -	03/2016	36	-6.11	i) Delay in Environment Clearance ii) Coal evacuation problem.
10	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,MADHYA PRADESH	06/2011	746.04 535.10	535.10	412.91	03/2015 -	03/2016	12	-28.27	i) Delay in Environment Clearance ii) Coal evacuation problem.

(November 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
11	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,TELANGANA	12/2009	212.34 1,228.39	1,228.39	861.82	03/2013 09/2012	03/2016	36	478.5	i)Delay in supply of LW equipment ii)Delay in drivage of gate roadways and installation of belt conveyors.
12	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35 -	462.35	298.87	03/2014 -	03/2016	24	0	Contractual Issues
13	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	67.34	03/2014 -	03/2016	24	0	Delay/ non issuance of 'Patta' for land/plots allotted to PAFs shifted and being shifted in the area acquired under CBA Act.
14	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	418.97	365.11	03/2012 -	03/2016	48	0	i) Land Acquisition ii) Rehabilitation & Resettlement Problems
15	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78 -	209.78	73.19	03/2015 -	03/2016	12	0	i) Delay in acquisition of forest land.
16	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	181.19	64.25	03/2012 -	03/2016	48	0	Environmental Clearance
17	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	35.96	03/2011 -	03/2016	60	0	hand over of forest land, NOC for diversion of Revenue Forest land from DC, Ranchi, Certificate under FRA,2006 is awaited
18	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	-	03/2013 -	03/2016	36	0	i)Rehabilitations &Resettlement Problems ii)Law & Order iii) Environmental Clearance
19	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	-	03/2012 -	03/2016	48	0	i)Environmental Clearance ii)others Problems
20	MURADIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	12.06	04/2014 -	03/2016	23	0	i) Environmental Clearance
21	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]NLC,TAMIL NADU	04/2012	364.75 -	364.75	182.79	10/2014 -	03/2016	17	0	i)Delay in land acquisition ii) Delay in supply of equipment, iii)Delay in civil works.
22	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	289.45	98.72	05/2014 -	10/2016	29	0	i)Delay in issue of Consent to Establish. ii) Delay in implementing project by BOM operator.
23	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	269.82	55.36	04/2014 -	11/2016	31	0	i)Delay in issue of Consent to Establish. ii) Delay in implementing project by BOM operator.

(November 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
24	ASHOK EXPN OCP CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	341.63 -	341.63	126.41	03/2011 -	03/2017	72	0	Authentication of land of Jhulundia ,Bijain Torhad ,Sidhalu, Thetangi and Lukaiya villages for 3621 acres.Authentication completed for 1600 acres.Balance pending at District Administration ,Chatra.
25	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL	11/2006	287.18 -	287.18	226.26	03/2011 -	03/2017	72	0	Processing of FC stage-I and stage-II was delayed by State Forest Deptt. and State Govt.
26	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 486.57	486.57	59.23	03/2012 03/2018	03/2017	60	87.58	i)Land Acquisition ii) Rehabilitations & Resettlement Problems
27	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	206.83	03/2013 -	03/2017	48	0	i) Environmental Clearance ii)Coal evacuation Problems
28	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	150.27	03/2010 -	03/2017	84	0	Rehabilitations & Resettlement Issues
29	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	453.63	101.64	12/2012 -	03/2017	51	0	i) Land Acquisition ii) Rehabilitations & Resettlement Problems iii)Contractual Issues iv)Adverse Geomining Conditions
30	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	205.79	03/2012 -	03/2017	60	0	i)Environmental Clearance ii)Delay in forest land Diversion
31	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	479.63	175.64	03/2013 -	03/2017	48	.02	Environmental Clearance
32	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	-	03/2012 -	03/2017	60	0	Rehabilitations &Resettlement Problems
33	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	70.05	03/2014 -	03/2017	36	0	i)Rehabilitations & Resettlement Problems ii)Environmental Clearance
34	RG OC -III EXTENSION (PHASE - II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	6.56	06/2015 -	03/2017	21	0	i) Land Acquisition ii) Rehabilitation & Resettlement Problems

(November 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
35	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL, TELANGANA	07/2012	417.33 -	417.33	14.13	07/2016 -	03/2017	8	0	Acquisition of non forest land and R&R
36	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL, TELANGANA	10/2006	249.03 -	249.03	76.65	03/2012 -	03/2018	72	0	i) Adverse Geo-mining condition.
37	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH	12/2009	321.50 -	321.50	209.59	03/2014 -	03/2018	48	0	Environmental Clearance
38	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29 -	242.29	0.03	03/2015 -	03/2018	36	0	i) Land Acquisition ii) Rehabilitation & Resettlement Problems iii) Delay in diversion of forest land.
39	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL, TELANGANA	07/2011	447.06 -	447.06	29.03	03/2015 -	03/2018	36	0	i) Land Acquisition ii) Rehabilitation & Resettlement Problems iii) Delay in diversion of forest land.
40	BAROUD OC EXPANSION (RCE)-3MTY - [N06000099]SECL, CHHATISGARH	04/2012	258.56 -	258.56	96.39	03/2016 -	03/2018	24	0	i) Land Acquisition ii) Delay in forestry clearance.
41	NEYVELI NEW THERMAL POWER PROJECT (2X500 MW) - [N06000095]NLC, TAMIL NADU	06/2011	5,907.11 -	5,907.11	1,204.77	12/2015 04/2018	04/2018	28	0	Delay in opening and evaluation of bids
42	RCE OF INDARAM OCP (1.20 MTPA) - [N06000093]SCCL, TELANGANA	07/2011	162.76 -	162.76	1.31	03/2015 -	03/2019	48	0	i) Land Acquisition ii) Rehabilitation & Resettlement Problems iii) Law & Order problem.
43	MOONIDIH XV SEAM UG - [N06000098]BCCL, JHARKHAND	08/2011	1,230.27 -	1,230.27	47.76	04/2015 04/2019	04/2019	48	0	i) Land Acquisition ii) Contractual issues.
44	TALABIRA OCP - [N06000043]MCL, ODISHA	03/2008	447.72 -	447.72	52.36	03/2016 -	03/2020	48	0	Delay in Environment and forestry Clearance.
45	JAGANNATHPOR OCP (3.00 MTY) - [N06000075]SECL, CHHATISGARH	09/2008	152.43 -	152.43	24.72	03/2015 -	03/2020	60	0	i) Land Acquisition ii) Rehabilitation & Resettlement Problems
46	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH	07/2008	178.44 -	178.44	0.30	03/2014 -	03/2020	72	0	i) Rehabilitation & Resettlement Problems ii) Environmental Clearance.
47	MAGADH OC 20 MTY (CCL) - [N06000015]CCL, JHARKHAND	08/2008	706.40 -	706.40	77.72	07/2012 -	03/2021	104	0	Law & Order

(November 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
48	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL, ODISHA	02/2008	395.87 -	395.87	-	03/2015 -	03/2021	72	0	i) Delay in Environment and forestry Clearance ii) Rehabilitation & Resettlement problem
	Total		24,482.34 -	25,466.46	10,104.66					
	<u>STEEL</u>									
49	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]SAIL, WEST BENGAL	11/2012	313.05 -	313.05	301.82	06/2015 -	12/2015	6	0	N.R.
50	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL, ODISHA	10/2012	160.48 -	160.48	142.58	09/2014 -	12/2015	15	0	N.R.
51	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHHATTISGARH - [N12000078]SAIL, CHHATTISGARH	07/2012	332.65 -	332.65	222.78	08/2014 -	01/2016	17	0	N.R.
52	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODISHA - [N12000079]SAIL, ODISHA	06/2012	237.09 -	237.09	216.21	12/2014 -	01/2016	13	0	N.R.
53	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL, MAHARASHTRA	12/2011	187.33 -	187.33	171.52	10/2013 -	03/2016	29	0	N.R.
54	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, CHHATTISGARH	08/2010	17,265.00 -	17,265.00	15,279.06	03/2013 -	06/2016	39	0	i) Shortcoming in design & engineering ii) Contractual Issues. iii) Inadequate resource mobilization by the contractor
55	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]JINL, ANDHRA PRADESH	07/2011	877.73 -	877.73	332.82	07/2015 -	06/2016	11	0	N.R.
56	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]SAIL, ODISHA	06/2014	708.91 -	708.91	245.17	04/2016 -	08/2016	4	0	N.R.
57	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC, CHHATTISGARH	01/2010	15,525.00 -	15,525.00	8,195.12	05/2015 12/2016	12/2016	19	0	N.R.
58	SMS-1 CONVERTERS REVAMPING - [N12000090]JINL, ANDHRA PRADESH	05/2012	404.16 -	404.16	248.15	07/2015 -	03/2017	20	0	N.R.

(November 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	Total		36,011.40 -	36,011.40	25,355.23					
	<u>PETROCHEMICALS</u>									
59	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, ASSAM	04/2006	5,460.61 8,920.00	9,965.00	9,025.14	04/2012 12/2013	12/2015	44	82.49	Significant changes in technology/ engineering/ operational/ utility requirements.
	Total		5,460.61 -	9,965.00	9,025.14					
	<u>PETROLEUM</u>									
60	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL, MAHARASHTRA	03/2012	1,419.00 -	1,419.00	1,284.80	12/2014 -	11/2015	11	0	Slow progress in construction activities
61	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL, ODISHA	07/2009	199.75 -	239.73	205.75	07/2013 11/2015	11/2015	28	20.02	Delay in DPR approval for ECOR
62	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]ONGC, MULTI STATE	10/2013	429.06 429.00	429.06	439.02	10/2014 10/2015	11/2015	13	0	Complication during drilling
63	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC, MULTI STATE	06/2010	2,523.00 2,523.00	2,523.00	1,658.41	01/2014 12/2015	12/2015	23	0	Delay in conversion work of Sagar Samrat to MOPU, slow progress by contractor.
64	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL, MULTI STATE	08/2011	586.00 -	586.00	400.66	08/2015 -	12/2015	4	0	Delay in acquisition of land at Balasore by Govt of Odisha for pump station construction has affected the project completion schedule.
65	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL, TAMIL NADU	12/2012	279.00 -	279.00	186.74	12/2014 -	12/2015	12	0	N.R.
66	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL, JHARKHAND	04/2011	191.96 -	191.96	96.98	05/2015 -	12/2015	7	0	delay in acquisition of additional land admeasuring 3.99 acre and limited availability of construction sand in Jharkhand due to existing regulations of State Government

(November 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
67	PARADIP REFINERY PROJECT - [N1600058]IOCL,ODISHA	02/2009	29,777.00 34,555.00	34,555.00	30,413.42	11/2012 11/2013	01/2016	38	16.05	Initial change in Front End Engg Design due to deferment of Petrochemicals lead to delayed detailed engg and subsequent procurement, Law & Order at site, Environment and Forest clearance of South Jetty and Pipeline, Delay in construction of Power Plant by BHEL, Delay in remobilization of manpower after cyclone Phailin struck Paradip in Oct' 13.
68	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	251.66	-	06/2012 11/2015	01/2016	43	-6.79	Court Case
69	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	1,250.50	09/2012 -	03/2016	42	0	Project is delayed due to receipt of Forest clearance, Law and order problems, Poor performance by contractors, Fund constraint of Contractor.
70	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA	12/2009	1,584.00 -	1,584.00	1,353.89	08/2015 -	03/2016	7	0	poor performance of the contractor, wild life clearance
71	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	463.32	314.41	06/2011 03/2012	03/2016	57	0	Delay in forest clearance, termination of contract, revised instruction for working /HDD of Chambal river
72	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	317.64 -	240.95	123.32	09/2012 12/2015	03/2016	42	-24.14	Slow progress in civil work and fabrication work due to less resource mobilization, Delay in finalization of Process package leading to delay in engg and procurement services.
73	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	1,016.37	10/2011 -	03/2016	53	67.62	issues faced with local elements in the RoU.
74	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,438.30	01/2012 -	03/2016	50	70.49	Progress is slow due to heavy rains during the period, RoU issue
75	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL,GUJARAT	12/2011	160.00 -	160.00	31.28	02/2016 02/2016	03/2016	1	0	NR

(November 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
76	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 1,256.72	1,256.72	989.16	05/2013 12/2015	04/2016	35	45.83	Increase in scope of work, Delay in procurement of steel and fabrication of legs by the contractor.
77	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	1,282.07	03/2015 05/2016	05/2016	14	29.42	contractual dispute
78	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 2,592.17	2,592.17	826.62	05/2014 05/2016	05/2016	24	0	Delay due to retendering, slow progress by contractor.
79	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17 600.17	600.17	375.14	12/2014 05/2015	05/2016	17	0	Pipeline package: Non-performance by the contractor
80	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE	01/2012	352.49 -	352.49	131.19	03/2014 05/2016	05/2016	26	0	Design platform integrity issue was raised by the contractor which required review of integrity analysis and this took time in resolution. Clubbing of project facilities alongwith C-26 Cluster development project, slow progress by the contractor.
81	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 686.58	686.58	540.72	04/2015 04/2015	05/2016	13	-39.69	NR
82	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	736.65	498.95	09/2011 12/2015	06/2016	57	0	Delay in preparation of drawing and additional model testing of Hull form in Austria. Shortage of skilled manpower at contractors' end.
83	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]IOCL,BIHAR	04/2013	480.00 -	480.00	85.08	02/2016 -	07/2016	5	0	retendering of mechanical tender
84	RESID UPGRADE PROJECT - [N16000184]CPCL,TAMIL NADU	02/2011	3,110.36 -	3,110.36	1,211.76	11/2015 07/2016	07/2016	8	0	Restricted working environment
85	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	1,200.00	432.84	03/2015 11/2015	08/2016	17	37.72	Heavy rain in Assam, Refloating of tender will have impact on timeline.
86	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,KARNATAKA	02/2012	666.00 838.08	838.08	546.07	11/2015 11/2016	11/2016	12	25.84	law and order, forest clearance

(November 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
87	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	913.00	455.18	08/2015 -	12/2016	16	0	Forest clearance and land acquisition.
88	CRU TO ISOMERIZATION (ISOM) - [N16000200]BPCL,MULTI STATE	10/2011	725.00 -	725.00	80.59	11/2016 -	12/2016	1	0	NR
89	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 2,378.89	2,378.89	1,789.38	03/2013 03/2016	03/2017	48	-3.5	ROU, Forest clearance, law & order
90	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 462.79	462.79	253.37	10/2014 03/2017	03/2017	29	49.38	Stiff resistance from villagers.
91	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC,MULTI STATE	04/2013	284.82 -	284.82	-	04/2015 05/2017	05/2017	25	0	Delay in tendering process
92	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]ONGC,MAHARASHTRA	12/2012	3,513.07 4,619.94	4,619.94	667.40	02/2016 12/2017	12/2017	22	31.51	Project has been dropped.
93	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE	05/2013	4,124.35 4,941.49	4,941.49	521.23	04/2016 12/2017	12/2017	20	19.81	Retendering of various packages.
94	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL, WEST BENGAL	03/2014	3,076.00 -	3,076.00	112.15	09/2017 -	12/2017	3	0	Due to high LSTK-1 quote, Execution methodology has been changed from LSTK to Hybrid which has impacted the schedule.
95	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	3,957.00 3,561.00	3,561.00	24.73	01/2013 -	12/2018	71	-10.01	No firm commitment from anchor load customers.
96	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI	08/2014	6,086.08 -	6,086.08	586.87	05/2019 03/2020	03/2020	10	0	NR
	Total		80,641.12 -	89,203.56	51,624.35					
	POWER									
97	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	342.05	02/2012 -	12/2015	46	0	Severe ROW problem in western UP.
98	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 1,007.57	1,007.57	947.62	07/2013 12/2015	12/2015	29	139.32	Commissioning delayed due to non-supply of requisite quantum of gas by ONGC. Subsequent activities like synchronization of the Steam Turbine is also delayed.

(November 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
99	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL, GUJARAT	12/2011	552.44 -	552.44	546.58	02/2014 -	12/2015	22	0	Severe ROW problem faced.
100	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL, MULTI STATE	03/2010	965.58 -	965.58	753.44	11/2012 -	01/2016	38	0	Severe ROW problem in western UP.
101	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL, ODISHA	09/2010	2,074.86 2,348.37	2,348.37	1,914.09	03/2013 06/2015	01/2016	34	13.18	Severe ROW problem at Angul end in Odisha.
102	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL, MULTI STATE	08/2010	1,677.57 -	1,677.57	1,436.11	04/2013 -	01/2016	33	0	Severe ROW problem in western UP.
103	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL, MULTI STATE	05/2010	250.03 -	250.03	184.17	01/2013 -	01/2016	36	0	Delayed due to delay in land acquisition.
104	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL, MULTI STATE	02/2012	1,927.16 -	1,927.16	1,564.24	10/2014 -	01/2016	15	0	Severe ROW problem.
105	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL, MULTI STATE	09/2012	524.40 -	524.40	269.39	05/2015 -	01/2016	8	0	Delayed due to delay in land acquisition.
106	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL, JHARKHAND	10/2011	558.26 -	558.26	489.81	11/2013 -	02/2016	27	0	Delay in land acquisition for Chandwa S/stn. & huge forest involvement.
107	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL, MULTI STATE	12/2011	2,422.66 -	2,422.66	2,301.62	08/2014 -	02/2016	18	0	Delay due to delay in land acquisition & ROW problem.
108	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL, MULTI STATE	12/2011	297.33 346.79	346.79	289.16	08/2014 06/2015	02/2016	18	16.63	Severe ROW problem in Bangalore area.
109	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL, MULTI STATE	12/2009	1,216.83 -	1,216.83	1,060.56	08/2012 -	03/2016	43	0	Contractual issues.
110	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL, MULTI STATE	03/2011	1,585.12 -	1,585.12	1,536.72	11/2013 -	03/2016	28	0	Severe ROW problem & forest clearance awaited.

(November 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
111	KBUNL-MUZAFFARPUR TPP STAGE-II- SUBSIDIARY (2X195 MW) - [N18000191]NTPC,BIHAR	03/2010	3,984.03 -	3,984.03	3,096.26	01/2013 -	03/2016	38	0	- Delay in completion of Project due to delay in land acquisition of Ash Dyke and ROU of MUW corridor. - Non performance of civil, Swyd, CHP, AHP agencies
112	BOKARO THERMAL POWER STATION-A - [N18000199]DVC,JHARKHAND	08/2006	2,313.00 4,139.00	4,237.67	3,088.00	12/2011 -	03/2016	51	83.21	NR
113	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99 1,487.49	1,487.49	1,074.08	08/2013 05/2016	05/2016	33	159.15	1) All activities of dam suspended w.e.f 7th June 2015 due to overtopping of coffer dam on 7th to 11th 14th, 23rd 27th to 28th June 2015 15th July 2015, 19th August 2015, 30.08.2015 to 3rd Sept 2015 and 24.09.2015. Dewatering completed & silt clearance is in progress. (2) Access to dam site is still restricted due to erosion of approach road.
114	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]NHPC,WEST BENGAL	09/2005	1,061.38 -	1,929.15	1,923.42	09/2009 -	06/2016	81	81.76	1. Initial delay in handing over of forest land & start of work 2. Bandh/ closure by locals , political outfits like GJMM and its effect 3. Due to inordinate delay and extended stay, BOQ rates become unworkable and resulted in cash deficit of Civil Contractor. 4. Delay in award of E&M contract due to clarification regarding participation of Chinese firm
115	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 721.81	721.81	555.26	09/2010 06/2013	06/2016	69	51.1	Severe ROW problem & forest clearance awaited.
116	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	500.24	11/2011 -	06/2016	55	0	Severe ROW problem in western UP.
117	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	2,219.30	12/2012 -	06/2016	42	0	Severe ROW problem & contractual issues.

(November 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
118	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL, MULTI STATE	07/2010	752.64 689.03	689.03	515.20	07/2013 11/2015	06/2016	35	-8.45	Forest clearance awaited & limited working period due to snow-bound area.
119	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL, CHHATTISGARH	05/2011	1,961.87 -	1,961.87	1,757.69	05/2014 -	06/2016	25	0	Delay due to delay in land acquisition for Champa Station.
120	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGY PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL, TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,864.76	09/2014 -	06/2016	21	0	Severe ROW problem & contractual issues.
121	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHHATTISGARH - [N18000112]PGCIL, CHHATTISGARH	11/2011	2,127.51 -	2,127.51	2,287.68	07/2014 -	06/2016	23	0	Forest clearance awaited & severe ROW problem.
122	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHHATTISGARH - [N18000116]PGCIL, CHHATTISGARH	12/2011	1,746.65 2,228.71	2,228.71	1,475.50	08/2014 12/2015	06/2016	22	27.6	Forest clearance delayed.
123	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL, CHHATTISGARH	01/2012	1,422.85 -	1,422.85	1,349.97	01/2015 -	06/2016	17	0	Delay in forest clearance.
124	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL, MULTI STATE	03/2012	198.63 -	198.63	90.74	09/2014 -	06/2016	21	0	Severe ROW problem faced during installation of OPGW.
125	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL, CHHATTISGARH	03/2012	9,569.76 -	9,569.76	5,312.24	06/2015 -	06/2016	12	0	Delay due to delay in land acquisition of Champa HVDC Station & forest clearance awaited.
126	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL, MULTI STATE	11/2011	723.63 -	723.63	554.56	11/2014 -	06/2016	19	0	Severe ROW problem in Uttarakhand & delay in forest clearance.
127	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL, MULTI STATE	02/2012	3,201.44 -	3,201.44	2,869.07	10/2014 -	06/2016	20	0	Delayed due to delay in land acquisition for Kanpur sub station.

(November 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
128	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 -	196.58	5.10	02/2016 -	06/2016	4	0	Completion delay due to delay in manufacturing of Reactors by M/s. BHEL.
129	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	277.30	06/2015 -	08/2016	14	0	NR
130	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	956.42	06/2015 -	08/2016	14	0	Forest clearance awaited & contractual issues.
131	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,497.72	4,276.75	01/2016 -	11/2016	10	50.95	Rehabilitation & Resettlement Plan is pending for approval with J&K State Govt.
132	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	5.36	04/2016 -	11/2016	7	0	Non-availability of PMU test lab worldwide and delay in amendment of stnd. IEEE C37.118. design.
133	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 6,476.34	6,476.34	4,252.71	12/2009 12/2016	12/2016	84	159.38	REASONS FOR DELAY: (1) Redesign of Dam parameter. (2) Geological surprise. (3) Realignment of HPT. (4) Slope Stabilization of Power House area. (5) Flash flood/rain. (6) Deviation in work. (7) Contractual issue. (8) Major deviation in encountered geology than that envisaged. (9) Quarry related issue with the Govt. Arunachal Pradesh. (10) Intermittent local law and order issues leading to loss of working days.
134	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	4,181.23	10/2012 -	12/2016	50	0	Forest clearance awaited & contractual issues.
135	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 -	4,404.57	2,357.96	01/2015 -	12/2016	23	0	Generation project delayed & delay in wildlife sanctuary clearance .

(November 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
136	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	1,219.55	11/2012 -	12/2016	49	0	Delay in sub stations land acquisition & ROW problem in LILO line.
137	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	1,043.56	12/2015 -	12/2016	12	0	Severe ROW problem & Hug forest involvement.
138	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]DVC, WEST BENGAL	04/2007	4,122.00 8,781.00	9,606.82	1,353.36	02/2011 -	01/2017	71	133.06	NR
139	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC, ASSAM	01/2008	4,375.35 6,749.18	6,749.18	5,588.00	09/2011 -	03/2017	66	54.25	- Poor performance of BOP/Civil contractors due to geo-political situation in the region. - Heavy rainfall leads to stoppage of work. - Frequent Bandh calls by local outfits (Total Bandh-272 days) leading to stoppage of work at site for more than 500 days.
140	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	01/2012	15,166.19 -	15,166.19	9,676.00	01/2017 -	03/2017	2	0	- NGT issue – work stopped from 17.03.14 to 01.04.14 - Work stoppage due to agitation against the project (5.07.14 to 22.07.14) - Delay in supply of Generator Stator of U#2 & 3 (M/s Toshiba)-
141	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	5,620.00	11/2016 -	08/2017	9	0	- Delay of 12 months in Engg. & supplies by BGR which has led to a consequent delay of 12 months in erection.
142	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 -	195.42	40.43	02/2014 -	09/2017	43	0	1.11KV power line has been constructed and poles have been erected. However, installation of transformers and charging of line is pending.
143	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	5,353.00	5,129.27	05/2014 -	09/2017	40	0	- Delay in balance land acquisition. - Law & order problem
144	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	4,233.50	12/2016 -	09/2017	9	0	- Delay of 12 months in Engg. & supplies by BGR which has led to a consequent delay of 12 months in erection.

(November 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
145	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO, MIZORAM	07/1998	368.72 1,381.71	1,381.71	910.21	07/2006 10/2017	10/2017	135	274.73	Poor approach road condition from Bhagabazar to Natanchera affecting seriously transportation of man, material, equipment and POL to project site. Work is affected due to rain and slippery road condition. As a result of constant pursuance by NEEPCO, the tonnage restriction of the vehicles carrying materials to the Tuirial project site has since been withdrawn by Assam Govt. w.e.f 30.11.2015
146	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL, MULTI STATE	02/2009	11,130.19 13,762.80	13,762.80	11,184.10	08/2013 12/2017	12/2017	52	23.65	Generation project delayed & law & order problem in NER.
147	BARH STPP(3X660MW) NTPC - [180100242]NTPC, BIHAR	02/2005	8,692.97 15,095.67	15,095.67	11,012.00	01/2011 10/2014	05/2018	88	73.65	Contractual issues
148	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC, HIMACHAL PRADESH	09/2002	3,919.59	7,818.68	5,328.26	09/2009	12/2018	111	99.48	1. Initial delay in start of Dam works due to delay in Revised Forest clearance 2. Burial of TBM during Nov, 06. Heavy ingress of water with silt from TBM face. Treatment of shear zone, 3. Back hill slope failure of Power House three times, 4. Ban on use of aggregates by Hon'ble High Court, Shimla

(November 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
149	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	2,631.00	03/2013 -	12/2018	69	29.14	- Unprecedented flood in Uttarakhand during Aug'12 and Jun'13 damaging cofferdam and approach roads. TBM stuck up thrice & L&T Alpine JV did not perform leading to termination of contract. - Head Race Tunnel (HRT) Package is under retender.
150	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	1,498.91	02/2016 02/2016	09/2019	43	79.77	4.668 Ha. Land diversion case for dumping area at Village Chopra.
151	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	2,491.58	752.82	06/2013 -	12/2019	78	0	NGT case
152	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	2,159.07	1,897.65	11/2008 03/2012	12/2016	97	21.34	Balance 01 line (Edaman-Muvattupuzha line) getting delayed due to severe ROW problem in Kerala. Work to start after assessment of compensation & payment by State Govt./KSEB. Compensation to be paid land value, to be finalised by concerned DC. Survey work restarted after panchayat election in Nov 15. However, resistance by land owner continues.
153	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 639.46	639.46	412.96	06/2014 03/2016	11/2015	17	31.17	Severe ROW problem.
	Total		153,605.70 -	189,246.33	130,013.94					
	HEAVY INDUSTRY									
154	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]HIPE,MULTI STATE	04/2011	1,718.00 -	3,827.30	-	09/2011 -	12/2017	75	122.78	Project is first of its kind so train man power is available in the country. NATRIP is temporary organization.
	Total		1,718.00 -	3,827.30	.00					
	HEALTH AND FAMILY WELFARE									

(November 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
155	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	175.57	89.92	12/2014 -	03/2016	15	0	N.R.
	Total		175.57 -	175.57	89.92					
	<u>RAILWAYS</u>									
156	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	335.00	230.67	06/2004 -	12/2015	138	72.62	Law & Order issue affected the work progress. Material Modification for Electrification estimate are awaited from Jharkhand Govt.
157	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 -	2,921.00	2,521.72	10/2007 12/2012	12/2015	98	367.76	Railway bridge targeted for commissioning in October, 2015. However Road bridge would take time as there are issues in land acquisition.
158	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	800.00	793.71	03/2010 -	12/2015	69	16.41	NR
159	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 495.44	1,781.98	440.08	03/2004 -	03/2016	144	259.68	Land acquisition
160	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	275.08	141.55	03/2012 12/2013	03/2016	48	60.77	Initially the electrification of Khurja-Meerut-Saharanpur section was sanctioned in 1996-97 and subsequently the work was frozen. In 2007-08 electrification work of Khurja-Meerut-Saharanpur was defroze and Ghaziabad-Meerut section also included as a material modification. Authorisation has been received on 13-08-2014 to run electric trains on Khurja-Meerut city. The electrification work on the balance portion is in progress and planned for completion by Nov 2015 (Meerut-Saharanpur).
161	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM	04/1998	227.90 200.00	331.40	182.22	12/2012 -	03/2016	39	45.41	NR

(November 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
162	LUMDING-SILCHAR, JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR, ASSAM	04/1996	1,676.31 -	5,500.00	4,734.45	03/2009 -	03/2016	84	228.1	Line commissioned and freight train operations commenced. Passenger operations to commence in August 2015.
163	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER, JHARKHAND	04/2010	309.44 388.67	583.00	144.66	12/2015 -	03/2016	3	88.4	NR
164	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR, TRIPURA	04/1999	895.00 575.00	1,242.25	1,005.81	03/2007 -	03/2016	108	38.8	Section will be completed after Lumding-Silchar, Badarpur- Kumarghat GC Project.
165	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	204.56	03/2016 -	06/2016	3	0	Work hampered due to encroachment on Railway land along the proposed metro alignment.
166	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER, ODISHA	04/2010	149.90 -	230.00	68.67	03/2015 -	12/2016	21	53.44	NR
167	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR, UTTAR PRADESH	04/2006	325.00 -	1,564.54	420.71	03/2010 03/2017	03/2017	84	381.4	NR
168	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	714.10	65.93	04/2016 -	03/2017	11	0	NR
169	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR, ASSAM	09/1997	1,500.00 1,000.00	4,996.19	3,410.06	04/2008 03/2014	06/2017	110	233.08	NR
170	KATI HAR - JOGBANI (GC)(NEFR) - [220100247]NFR, BIHAR	09/2001	492.98 -	1,727.27	743.74	12/2010 -	03/2018	87	250.37	Work affected due to fund constraint.
171	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	733.00 733.00	2,531.34	1,732.43	12/2008 -	03/2018	111	245.34	Work is affected due to land problems. State Govt. has been requested to expedite handing over of land to Railways for early commissioning of the line.
172	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA	04/2008	813.34 813.34	2,876.00	823.83	03/2014 -	03/2018	48	253.6	Supreme court approval is required for NBWL clearance of 9.94 Hect Trishna Wild life Sanctuary.
173	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	619.34 619.34	2,820.25	199.31	04/2014 03/2015	03/2018	47	355.36	NR
174	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	4,874.58	1,911.65	03/2016 -	06/2018	27	0	Project progress depends on availability of land and funds.

(November 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
175	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	19,565.00	10,658.34	11/2002 -	12/2018	193	682.6	Delayed due to change in alignment and court case.
176	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 727.56	6,570.75	2,787.99	03/2011 03/2014	03/2019	96	803.12	NR
177	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 6,821.29	7,986.04	2,443.62	03/2014 03/2019	03/2019	60	50.68	Fund constraint affecting the progress of projects.
178	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,157.54	1,544.40	590.26	03/1998 -	12/2019	261	299.79	Progress is going as per the allotment of budget grant.
179	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,WEST BENGAL	03/1998	111.90 1,039.29	2,371.85	486.25	03/2005 12/2008	12/2019	177	2019.62	Local disturbance and fund constraint affected the work progress.
180	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 1,013.74	1,428.00	466.36	06/2005 07/2011	12/2019	174	385.76	In Kanthi-Egra section land acquisition is kept in abeyance due to insufficient funds and no interest showing by the State Govt.
181	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 1,339.48	4,190.00	88.56	12/2015 -	03/2020	51	212.81	Delay in land acquisition affected work progress in Rongchong and Kalimpong (West Bengal).
182	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00 -	2,973.42	10.44	03/2015 03/2020	03/2020	60	249.81	Land acquisition is pending.
	Total		29,410.10 -	85,131.16	37,307.58					
	<u>ROAD TRANSPORT AND HIGHWAYS</u>									
183	GUWAHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	175.96	182.50	04/2008 12/2015	12/2015	92	0	N.R.
184	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	198.16	-	04/2008 12/2015	12/2015	92	0	N.R.
185	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	197.60	05/2008 12/2015	12/2015	91	0	Land acquisition, Utility shifting, Pending railway clearance
186	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	309.56	258.40	04/2010 02/2016	02/2016	70	42.25	N.R.
187	SONAPUR TO GUWAHATI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	245.00	491.20	03/2008 04/2016	04/2016	97	0	N.R.
188	NALBARI TO BIJUNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	258.40	06/2008 04/2016	04/2016	94	0	N.R.

(November 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
189	REHABILITATION & UPGRADE OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) T - [N24000267]PWD,ANDHRA PRADESH	02/2014	258.99 -	258.99	64.65	07/2014 -	07/2016	24	0	N.R.
190	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	208.00	290.60	04/2008 01/2017	01/2017	105	0	N.R.
191	REHABILITATION UPGRADE OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH	07/2014	251.55 -	251.55	-	02/2015 -	02/2017	24	0	N.R.
	Total		1,940.27 -	2,032.22	1,743.35					
	<u>SHIPPING AND PORTS</u>									
192	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	600.00	139.80	03/2006 -	12/2015	117	300	i)Encroachment
193	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 669.46	669.46	412.00	12/2010 -	01/2016	61	82.72	poor performance of contractor
194	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 373.22	409.83	353.18	04/2009 03/2010	08/2016	88	66.82	Land acquisition problem.
195	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 -	1,460.00	1,038.00	12/2010 -	09/2017	81	18.89	Delay due to scrutiny of technical bid.
	Total		1,990.06 -	3,139.29	1,942.98					
	<u>TELECOMMUNICATIONS</u>									

(November 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
196	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	384.00	74.74	10/2010 08/2015	11/2015	61	0	i) Issue related to change of business process. ii) FIT issue iii) Integration issue with CDR system iv) Issue related to procurement of additional server storage.
	Total		384.00 -	384.00	74.74					
	URBAN DEVELOPMENT									
197	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD,WEST BENGAL	01/2009	225.81 -	225.81	136.53	06/2012 12/2015	12/2015	42	0	N.R.
198	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	12/2015	11	0	N.R.
199	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	884.30	-	08/2014 -	01/2016	17	0	N.R.
200	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	57.69	11/2014 -	03/2016	16	0	N.R.
201	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI	05/2012	405.01 -	405.01	-	12/2014 -	04/2016	16	0	N.R.
202	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 171.86	171.86	8.64	03/2016 -	05/2016	2	0	N.R.
203	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85 -	261.85	150.77	05/2013 10/2015	06/2016	37	0	N.R.
204	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 14,600.00	14,600.00	11,544.24	12/2015 -	08/2016	8	0	N.R.

(November 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
205	DELHI MRTS PHASE-III - [N28000056]DMRCL, DELHI	09/2011	38,585.00 -	38,585.00	18,738.92	03/2016 -	12/2016	9	0	Rehabilitation & Resettlement, Land acquisition and Delay in technical approval from M/o Railways delays the project.
206	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD, MADHYA PRADESH	12/2012	188.87 -	188.87	5.79	12/2014 -	12/2016	24	0	N.R.
207	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD, WEST BENGAL	02/2014	156.57 -	156.57	18.65	09/2015 07/2016	12/2016	15	0	N.R.
208	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD, TAMIL NADU	04/2014	332.72 -	332.72	58.72	09/2016 01/2017	01/2017	4	0	N.R.
	Total		79,218.82 -	79,218.82	30,719.95					
	Grand Total		455,789.45	576,028.57	332,124.65					

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(November 2015)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	09/2016	62.57	72
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	22,462.00	12/2008 -	06/2016	70.54	90
	Total		16,663.00 -	28,139.00				
	<u>COAL</u>							
3	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	03/2016	478.50	36
4	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI [N06000033]	10/2007	259.40 -	486.57	03/2012 -	03/2017	87.58	60
5	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	479.63	03/2013 -	03/2017	0.02	48
	Total		951.27 -	2,194.59				
	<u>HEAVY INDUSTRY</u>							
6	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78	75
	Total		1,718.00 -	3,827.30				
	<u>PETROCHEMICALS</u>							
7	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	9,965.00	04/2012 -	12/2015	82.49	44
	Total		5,460.61 -	9,965.00				
	<u>PETROLEUM</u>							
8	MARKETING TERMINAL AT PARADEEP - [N16000168]	07/2009	199.75 -	239.73	07/2013 -	11/2015	20.02	28
9	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79	10/2014 -	03/2017	49.38	29
10	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) [N16000146]	02/2012	666.00 -	838.08	11/2015 -	11/2016	25.84	12
11	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE [N16000157]	01/2006	732.00 -	1,227.00	10/2011 -	03/2016	67.62	53

(November 2015)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
12	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128	03/2011	861.79 -	1,256.72	05/2013 -	04/2016	45.83	35
13	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148	09/2012	871.35 -	1,200.00	03/2015 -	08/2016	37.72	17
14	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169	01/2006	993.00 -	1,693.00	01/2012 -	03/2016	70.49	50
15	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131	12/2011	2,059.63 -	2,665.65	03/2015 -	05/2016	29.42	14
16	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160	12/2012	3,513.07 -	4,619.94	02/2016 -	12/2017	31.51	22
17	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172	05/2013	4,124.35 -	4,941.49	04/2016 -	12/2017	19.81	20
18	PARADIP REFINERY PROJECT - [N16000058	02/2009	29,777.00 -	34,555.00	11/2012 -	01/2016	16.05	38
	Total		44,107.75 -	53,699.40				
	<u>POWER</u>							
19	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115	12/2011	297.33 -	346.79	08/2014 -	02/2016	16.63	18
20	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119	07/1998	368.72 -	1,381.71	07/2006 02/2015	10/2017	274.73	135
21	TRIPURA GAS BASED POWER PROJECT - [N18000071	07/2009	421.01 -	1,007.57	07/2013 -	12/2015	139.32	29
22	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035	12/2007	477.69 -	721.81	09/2010 -	06/2016	51.10	69
23	PARE HYDRO ELECTRIC PROJECT - [N18000045	12/2008	573.99 -	1,487.49	08/2013 -	05/2016	159.15	33
24	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243	09/2005	1,061.38 -	1,929.15	09/2009 -	06/2016	81.76	81
25	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	07/2006	1,657.00 -	2,978.86	02/2016 -	09/2019	79.77	43
26	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116	12/2011	1,746.65 -	2,228.71	08/2014 -	06/2016	27.60	22
27	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087	09/2010	2,074.86 -	2,348.37	03/2013 -	01/2016	13.18	34
28	BOKARO THERMAL POWER STATION-A - [N18000199	08/2006	2,313.00 4,139.00	4,237.67	12/2011 -	03/2016	83.21	51
29	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239	12/2004	2,496.90 -	6,476.34	12/2009 06/2016	12/2016	159.38	84
30	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014	11/2006	2,978.48 -	3,846.30	03/2013 -	12/2018	29.14	69
31	KISHANGANGA HEP (3X110 MW) - [N18000031	01/2009	3,642.04 -	5,497.72	01/2016 -	11/2016	50.95	10

(November 2015)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
32	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	7,818.68	09/2009 -	12/2018	99.48	111
33	RAGHUNATHPUR THERMAL POWER STATION PHASE-I [N18000202]	04/2007	4,122.00 8,781.00	9,606.82	02/2011 -	01/2017	133.06	71
34	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	6,749.18	09/2011 -	03/2017	54.25	66
35	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	15,095.67	01/2011 -	05/2018	73.65	88
36	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	13,762.80	08/2013 -	12/2017	23.65	52
	Total		52,349.15 -	87,521.64				
	<u>RAILWAYS</u>							
37	BANKURA - DAMODAR (GC) (SER) - [220100277]	03/1998	111.90 -	2,371.85	03/2005 12/2008	12/2019	2,019.62	177
38	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION [N22000162]	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44	21
39	ELECTRIFICATION OF KHURJA-MEERUT- SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	03/2016	60.77	48
40	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	194.07 -	335.00	06/2004 -	12/2015	72.62	138
41	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41	39
42	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,428.00	06/2005 -	12/2019	385.76	174
43	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	03/2016	88.40	3
44	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,564.54	03/2010 -	03/2017	381.40	84
45	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30 -	1,544.40	03/1998 -	12/2019	299.79	261
46	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	492.98 -	1,727.27	12/2010 -	03/2018	250.37	87
47	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	1,781.98	03/2004 -	03/2016	259.68	144
48	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,820.25	04/2014 -	03/2018	355.36	47
49	PATNA GANGA BRIDGE (NL), ECR - [220100308]	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76	98
50	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41	69
51	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	6,570.75	03/2011 -	03/2019	803.12	96

(November 2015)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
52	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [N20100266	04/2000	733.00 -	2,531.34	12/2008 -	03/2018	245.34	111
53	AGARTALA SABROOM, NL, NEFR - [N22000099	04/2008	813.34 -	2,876.00	03/2014 -	03/2018	253.60	48
54	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124	04/2006	850.00 -	2,973.42	03/2015 -	03/2020	249.81	60
55	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194	04/1999	895.00 -	1,242.25	03/2007 -	03/2016	38.80	108
56	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	4,190.00	12/2015 -	03/2020	212.81	51
57	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [N20100201	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	06/2017	233.08	110
58	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127	04/1996	1,676.31 -	5,500.00	03/2009 -	03/2016	228.10	84
59	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [N20100133	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60	193
60	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68	60
	Total		21,423.70 -	77,144.76				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
61	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063	12/2003	217.61 -	309.56	04/2010 -	02/2016	42.25	70
	Total		217.61 -	309.56				
	<u>SHIPPING AND PORTS</u>							
62	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	12/2015	300.00	117
63	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059	03/2007	245.67 -	409.83	04/2009 -	08/2016	66.82	88
64	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	01/2007	366.39 -	669.46	12/2010 -	01/2016	82.72	61
65	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016	11/2007	1,228.00 -	1,460.00	12/2010 -	09/2017	18.89	81
	Total		1,990.06 -	3,139.29				
	Grand Total		144,881.15	265,940.54				

Details of Projects Without Date of Commissioning

Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)	
				Original / Revised	Anticipated
1	2	3	4	5	6
	<u>CIVIL AVIATION</u>				
1	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 -	05/2012 -	03/2015
2	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	03/2014 -	05/2015
3	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	03/2015 -	09/2015
	Total		897.49 -		
	<u>COAL</u>				
4	JALLARAM SHAFT PROJECT - [N06000025]SCCL,TELANGANA	09/2007	467.78 -	03/2013 -	-
	Total		467.78 -		
	<u>STEEL</u>				
5	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,KARNATAKA	04/2011	572.00 -	04/2013 09/2014	06/2015
6	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,KARNATAKA	02/2011	898.55 -	05/2013 01/2015	08/2015
7	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH	04/2014	188.93 -	04/2015 -	-
	Total		1,659.48 -		
	<u>PETROLEUM</u>				
8	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00 -	12/2012 -	06/2015
9	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	- -	-
10	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	- -	-
11	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 -	- -	-
12	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00 -	- -	-
13	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE	02/2015	890.00 -	- -	-
14	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 -	01/2014 -	-
	Total		9,034.77 -		
	<u>POWER</u>				

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
15	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC, ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-
16	SYSTEM STRENGTHENING XII OF SR - [N18000085]PGCIL, MULTI STATE	02/2010	232.34 -	06/2012 -	-
17	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL, ANDHRA PRADESH	03/2012	206.44 -	06/2014 -	-
	Total		6,724.11 -		
	<u>HEALTH AND FAMILY WELFARE</u>				
18	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC, DELHI	02/2013	414.11 -	11/2013 -	11/2014
19	AIIMS-RAEBARELI-HOUSING - [N21000006]HSCC, UTTAR PRADESH	10/2013	159.50 -	11/2013 -	09/2015
	Total		573.61 -		
	<u>RAILWAYS</u>				
20	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR, TELANGANA	07/1998	125.00 -	07/2008 -	07/2008
21	KODERMA GIRIDH (NL), ECR - [220100306]ECR, JHARKHAND	04/1996	768.87 -	- 03/2010	03/2010
22	CALICUT-MANGALORE (DL) (SR) - [220100151]SR, MULTI STATE	02/1996	240.00 -	- -	02/2012
23	AMRAVATI-NARKHER NL(CR) - [220100118]CR, MAHARASHTRA	06/1994	663.01 663.01	06/1999 -	07/2012
24	JIND-SONEPAT (NL), NR - [220100280]NR, HARYANA	01/2004	238.56 -	03/2012 03/2012	12/2012
25	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRT, TAMIL NADU	04/2006	495.74 -	06/2013 06/2013	06/2013
26	GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL	04/2009	611.03 -	12/2011 11/2013	11/2013
27	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, TELANGANA	12/1994	124.43 -	- -	02/2014
28	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER, MULTI STATE	04/2009	257.42 -	03/2014 -	03/2014
29	CUTTACK - BARANG (LD) - [220100326]RVNL, ODISHA	04/1995	127.13 -	- 10/2014	10/2014
30	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER, WEST BENGAL	04/2010	171.02 -	06/2013 -	01/2015
31	PANVEL PEN DOUBLING - [N22000255]CR, MULTI STATE	04/2006	96.16 -	- -	01/2015
32	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR, MULTI STATE	04/1986	158.77 608.02	03/1994 -	03/2015
33	NANDYAL-YERRAGUNTALA(NL), SCR - [220100192]SCR, ANDHRA PRADESH	03/1996	155.74 164.36	02/2009 -	03/2015
34	MUNEERABAD-MAHABOBNAGAR(NL), SCR - [220100205]SCR, MULTI STATE	04/1997	218.24 236.41	- -	03/2015
35	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, WEST BENGAL	04/1974	393.46 393.46	03/2007 03/2007	03/2015

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
36	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	- 05/2009	03/2015
37	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	03/2015 -	03/2015
38	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00 -	- -	03/2015
39	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 -	03/2015 -	03/2015
40	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	98.74 -	- -	03/2015
41	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	12/2009 03/2011	06/2015
42	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	03/2013 -	09/2015
43	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 -	12/2012 -	09/2015
44	HOSADURGA - CHICKAJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA	04/2010	203.40 -	- -	09/2015
45	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 -	03/2009 12/2012	10/2015
46	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 245.39	12/2008 -	10/2015
47	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	02/2009 02/2009	-
48	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 -	- 03/2010	-
49	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-
50	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	12/2011 12/2010	-
51	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	- -	-
52	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 -	- -	-
53	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	- -	-
54	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-
55	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-
56	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	- -	-
57	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	2,957.21 -	07/2005 -	-
58	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	05/2008 -	-
59	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 501.69	03/2012 -	-
60	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
61	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-
62	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-
63	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 -	- -	-
64	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE	03/1998	280.00 -	- -	-
65	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	- -	-
66	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 3,385.14	12/2006 -	-
67	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	02/2011 02/2011	-
68	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	- 12/2009	-
69	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-
70	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 -	- -	-
71	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	- -	-
72	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	- 09/2009	-
73	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-
74	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-
75	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-
76	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-
77	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	- -	-
78	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	- -	-
79	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	02/2015 -	-
80	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	03/2009 03/2009	-
81	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	- -	-
82	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-
83	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 332.92	03/2012 -	-
84	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N220000032]SCR,TELANGANA	04/2006	378.56 -	- -	-
85	GOELKERA-MANOHARPUR,(LD)(SER) - [N220000045]SER,JHARKHAND	03/1997	261.70 -	02/2006 -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
86	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-
87	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	03/2010 -	-
88	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	- -	-
89	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE	12/2006	170.00 -	03/2011 -	-
90	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 -	- -	-
91	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 -	- -	-
92	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	1,106.62 -	12/2010 -	-
93	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	-
94	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	03/2014 -	-
95	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 732.06	03/2014 -	-
96	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	-
97	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	533.38 -	12/2011 -	-
98	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	293.74 -	12/2010 -	-
99	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-
100	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	03/2013 -	-
101	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	03/2014 -	-
102	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	-
103	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-
104	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
105	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	-
106	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	-
107	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	- -	-
108	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	- -	-
109	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
110	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
111	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-
112	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	- -	-
113	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	- -	-
114	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	- -	-
115	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-
116	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 913.48	- -	-
117	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT	04/2013	1,266.89 -	- -	-
118	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	- -	-
119	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	- -	-
120	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-
121	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	-
122	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
123	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
124	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	- -	-
125	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	- -	-
126	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	- -	-
127	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	- -	-
128	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	- -	-
129	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	- -	-
130	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	- -	-
131	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL	04/2011	289.64 -	- -	-
132	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	- -	-
133	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-
134	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-
135	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
136	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-
137	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-
138	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-
139	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-
140	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-
141	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-
142	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-
143	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-
144	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-
145	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
146	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-
147	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS (NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-
148	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-
149	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	- -	-
150	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-
151	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
152	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-
153	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-
154	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	- -	-
155	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-
156	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
157	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
158	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-
159	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-
160	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
161	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-
162	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-
163	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	- -	-
164	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-
165	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-
166	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-
167	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-
168	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-
169	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-
170	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-
171	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-
172	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-
173	SONDALIA-CHAMPAPUR DOUBLING WITH NEW MM FOR BIRACHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-
174	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-
175	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-
176	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	- -	-
177	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-
178	BARIARPIUR-MANANPUR VIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-
179	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-
180	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-
181	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-
182	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-
183	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
184	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-
185	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-
186	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-
187	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	- -	-
188	SANTOSHPUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-
189	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-
190	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-
191	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-
192	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-
193	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	- -	-
194	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-
195	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE	04/2013	723.00 -	- -	-
196	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 -	- -	-
197	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE	04/2008	184.26 -	- -	-
198	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-
199	GUDUR-DURGARAJPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-
200	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-
201	MANSABHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-
202	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-
203	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-
204	DELHI-SOHA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-
205	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-
206	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-
207	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
208	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	-
209	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-
210	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-
211	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	- -	-
212	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-
213	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-
214	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
215	MUDKHED-PARBHANI - [N22000283]SCR,MAHARASHTRA	04/2011	390.60 -	- -	-
216	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	- -	-
217	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49 -	- -	-
218	KADAPA-BANGALORE (NL), KADAPA-PENDIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	- -	-
219	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
220	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-
221	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-
222	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-
223	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-
224	UNCHAHAAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-
225	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-
226	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-
227	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	- -	-
228	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-
229	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	- -	-
230	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	-
231	MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-
232	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-
233	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	01/1999 -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
234	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 -	-
235	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-
236	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	01/1999 -	-
237	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-
238	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	- -	-
239	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 -	- -	-
240	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 -	- -	-
241	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	- -	-
242	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	03/2015 -	03/2015
243	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-
244	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR,TAMIL NADU	04/2011	190.10 -	- -	-
245	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,900.00 -	- -	-
246	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	- -	-
247	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 -	- -	-
248	YELAHANKA-PENKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	- -	-
249	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-
250	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-
251	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA	05/2015	400.00 -	- -	-
252	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA	03/2015	960.00 -	- -	-
253	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 -	- -	-
254	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	720.00 -	- -	-
	Total		114,215.44 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
255	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH	12/2014	201.12 201.00	02/2015 -	02/2015
256	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA	10/2013	283.25 -	10/2015 -	10/2015

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
257	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 -	09/2007 -	-
258	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	09/2008 -	-
259	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	06/2005 -	-
260	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	10/2008 -	-
261	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	-
262	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	-
263	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	-
264	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-
265	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	04/2009 -	-
266	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	06/2008 -	-
267	BIJNI TO ASSAM /WB BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	06/2008 -	-
268	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	09/2008 -	-
269	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	10/2008 -	-
270	RAJMARG CHORAH TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	10/2008 -	-
271	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	07/2008 -	-
272	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-
273	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	06/2008 -	-
274	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-
275	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 -	09/2007 -	-
276	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	-
277	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	02/2010 -	-
278	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-
279	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	09/2007 -	-
280	NH CONNECTIVITY TO ICTT VALLARPADAUE NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	02/2010 -	-
281	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	09/2010 -	-
282	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
283	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	07/2012 -	-
284	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT	03/2010	1,509.10 -	09/2012 -	-
285	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	05/2012 -	-
286	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	10/2011 -	-
287	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	08/2011 -	-
288	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	10/2011 -	-
289	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	-
290	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	12/2012 -	-
291	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	-
292	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	- -	-
293	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	09/2013 -	-
294	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	-
295	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	01/2013 -	-
296	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA	02/2010	390.56 -	02/2012 -	-
297	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	03/2013 -	-
298	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	-
299	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,KARNATAKA	09/2010	671.00 -	- -	-
300	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	07/2013 -	-
301	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	-
302	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	11/2012 -	-
303	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00 -	10/2014 -	-
304	DEVIHALLI-HASSAN - [N24000152]NHAI,KARNATAKA	12/2010	453.00 -	- -	-
305	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	09/2013 -	-
306	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	06/2013 -	-
307	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-
308	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
309	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,KARNATAKA	12/2010	480.00 -	- -	-
310	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-
311	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,KARNATAKA	11/2010	680.00 -	- -	-
312	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	-
313	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-
314	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-
315	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	-
316	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	-
317	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT	12/2010	1,008.50 -	06/2013 -	-
318	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,GUJARAT	03/2011	785.50 -	08/2013 -	-
319	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	-
320	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-
321	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	12/2013 -	-
322	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	-
323	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	-
324	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	-
325	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	-
326	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	-
327	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-
328	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	03/2013 -	-
329	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	01/2014 -	-
330	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	02/2014 -	-
331	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014 -	-
332	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	-
333	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	02/2014 -	-
334	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
335	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-
336	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	-
337	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	-
338	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	-
339	2LANING WITH PS GOPALGANJ-CHAPRA - [N24000190]NHAI,BIHAR	12/2011	325.00 -	05/2014 -	-
340	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	02/2014 -	-
341	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	01/2013 -	-
342	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	01/2014 -	-
343	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	01/2014 -	-
344	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	08/2013 -	-
345	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	05/2014 -	-
346	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	-
347	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	02/2013 -	-
348	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	06/2014 -	-
349	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	-
350	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	-
351	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	08/2013 -	-
352	4-LANING OF BRAHAMPUR-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	08/2013 -	-
353	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	08/2013 -	-
354	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	06/2014 -	-
355	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	-
356	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	07/2012 -	-
357	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	-
358	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	07/2014 -	-
359	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19 -	10/2014 -	-
360	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	07/2014 -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
361	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	10/2013 -	-
362	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	04/2014 -	-
363	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	10/2013 -	-
364	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,MULTI STATE	12/2012	1,479.00 -	06/2015 -	-
365	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	06/2014 -	-
366	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00 -	08/2015 -	-
367	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-
368	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH	10/2012	250.50 -	10/2014 -	-
369	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	07/2014 -	-
370	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	04/2015 -	-
371	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT	03/2012	828.00 -	09/2014 -	-
372	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN	03/2012	333.51 -	09/2014 -	-
373	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	02/2015 -	-
374	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	02/2014 -	-
375	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI,ANDHRA PRADESH	09/2013	606.00 -	- -	-
376	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI,TELANGANA	04/2014	1,123.17 -	- -	-
377	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA	03/2015	298.33 -	- -	-
378	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD TO FO - [N24000258]DORTH,GOA	03/2015	184.05 -	- -	-
379	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA	03/2015	280.16 -	- -	-
380	REHABILITATION AND UPGRADE OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH	03/2015	175.03 -	- -	-
	Total		91,542.28 -		
	SHIPPING AND PORTS				
381	ACQUISITION OF TWO (2) NOS OF 317000 DWT VLCC'S FROM JIANGSU RONGSHENG HEAVY INDUSTRIES CO.LTD.,CHIN - [N25000064]SHIPP.,MAHARASHTRA	10/2010	994.82 -	11/2013 -	11/2013

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
382	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-
	Total		3,422.22 -		
	<u>TELECOMMUNICATIONS</u>				
383	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	07/2015 -	-
	Total		13,334.00 -		
	<u>URBAN DEVELOPMENT</u>				
384	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB	02/2014	388.00 -	01/2015 -	01/2015
385	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CENTRA - [N28000089]CPWD,TAMIL NADU	12/2015	209.00 -	- -	-
386	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA	05/2006	6,395.00 -	06/2011 -	-
387	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]CPWD,BIHAR	02/2012	171.10 -	09/2014 -	-
388	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI - [N28000064]CPWD,DELHI	01/2010	162.90 -	07/2012 -	-
389	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD,ODISHA	11/2012	238.43 -	02/2015 -	-
390	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 -	11/2014 -	-
391	CONSTRUCTION OF MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB - [N28000070]CPWD,PUNJAB	08/2005	191.24 -	08/2007 -	-
392	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	03/2012 -	-
393	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 -	06/2015 -	-
394	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	10/2012 -	-
395	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA - [N28000078]CPWD,BIHAR	11/2006	2,727.89 -	03/2010 -	-
396	REHABILITATION AND STRENGTHENING OF SEWEWRAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI(IN ZONE 2 IN - [N28000082]JnNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-
	Total		11,657.02 -		
	Grand Total		253,528.20		

Details of Projects Without Original Date of Commissioning

(November 2015)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>CIVIL AVIATION</u>								
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	314.61	18.02	- -	09/2018	-	0/0
	Total		314.61 -	314.61	18.02				0/0
	<u>RAILWAYS</u>								
2	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	744.71 -	744.71	576.86	- -	03/2016	-	0/1
3	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	914.98	846.18	- -	03/2016	-	0/0
4	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	155.81	18.25	- -	12/2016	-	0/0
5	RAMGANJUMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	470.92 727.13	1,225.90	257.59	- -	03/2017	-	0/0
6	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 663.67	1,101.16	194.91	- -	03/2017	-	0/0
7	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	200.00 200.00	496.24	213.72	- -	03/2017	-	0/0
8	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 210.00	394.28	233.46	- -	03/2017	-	0/0
9	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 315.13	365.00	2.52	- -	12/2017	-	0/0
10	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,062.36	1,651.54	1,621.40	- -	03/2018	-	0/0
11	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	282.92 282.92	565.13	2.80	- 03/2014	03/2018	48(R3)	0/0
12	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	252.00 -	886.65	-	- -	03/2018	-	0/0
13	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR,WEST BENGAL	04/2011	209.77 190.39	441.45	85.78	- -	03/2018	-	0/0
14	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR,WEST BENGAL	04/2012	283.55 278.21	288.81	11.74	- -	03/2018	-	0/0
15	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 171.00	679.57	40.41	- -	03/2018	-	0/0
16	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	165.82 165.82	435.58	0.56	- -	03/2018	-	0/0

(November 2015)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
17	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWAJAI - [N22000209]NFR,MULTI STATE	04/1999	523.17 380.60	1,653.55	1,040.11	- -	03/2018	-	0/0
18	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	312.12 257.93	453.10	134.79	- -	03/2018	-	0/0
19	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 -	1,143.60	189.12	- -	03/2018	-	0/0
20	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	36.80 36.38	1,336.57	255.55	- -	03/2019	-	0/0
21	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	300.00 300.00	827.73	53.52	- -	03/2019	-	0/0
22	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 1,798.00	1,887.90	-	- -	03/2019	-	0/0
23	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL	04/2010	221.42 205.31	563.13	22.39	- -	03/2019	-	0/0
24	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM	04/2012	246.07 246.07	364.06	0.30	- -	03/2019	-	0/0
25	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 651.17	1,009.00	7.50	- -	12/2019	-	0/0
26	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	4,487.70	-	- -	03/2020	-	0/0
27	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	4,083.02 -	5,307.90	7.79	- 03/2016	03/2020	48(R3)	0/0
	Total		18,087.17 -	29,381.05	5,817.25				0/1
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
28	REHABILITATION & UPGRADE OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA	01/2014	446.77 -	446.77	-	- -	06/2017	-	0/0
29	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]NHDP,GOA	03/2015	297.00 -	297.00	-	- -	10/2017	-	0/0
30	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA	03/2015	168.30 -	168.30	-	- -	10/2017	-	0/0
	Total		912.07 -	912.07	.00				0/0
	Grand Total		19,313.85	30,607.73	5,835.27				0/1

Details of Projects Without Milestones w.r.t. Original Schedule

(November 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Antici Pated	
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
1	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 -	05/2012 -	03/2015	0/0
2	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	03/2014 -	05/2015	0/0
3	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	03/2015 -	09/2015	0/0
4	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	01/2011 06/2016	09/2017	0/0
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	- -	09/2018	0/0
	Total		1,521.56 -			0/0
	<u>COAL</u>					
6	AMGAON OPENCAST PROJECT RCE - [N06000135]SECL,CHHATISGARH	07/2015	316.10 -	03/2020 -	03/2020	0/0
7	BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH	07/2015	231.92 -	03/2022 -	03/2022	0/0
8	DURGAPUR OPENCAST PROJECT - [N06000136]SECL,CHHATISGARH	02/2015	916.24 -	03/2023 -	03/2023	0/0
	Total		1,464.26 -			0/0
	<u>FERTILISERS</u>					
9	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79 197.79	11/2016 -	11/2016	0/0
	Total		197.79 -			0/0
	<u>MINES</u>					
10	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]JHCL,MADHYA PRADESH	09/2011	1,856.00 -	09/2017 -	09/2017	0/0
	Total		1,856.00 -			0/0
	<u>STEEL</u>					
11	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	10/2016 -	10/2016	0/0
12	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND	02/2014	4,749.00 -	09/2017 -	09/2017	0/0

(November 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
13	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	10/2017 -	10/2017	0/0
14	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND	05/2015	1,154.18 -	12/2017 -	12/2017	0/0
15	ALTERNATE GAS NETWORK AT BSL - [N12000093]SAIL,JHARKHAND	03/2015	255.19 -	03/2018 -	03/2018	0/0
16	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA	04/2015	3,127.30 -	04/2018 -	04/2018	0/0
	Total		10,662.68 -			0/0
	<u>PETROLEUM</u>					
17	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]ONGC,MULTI STATE	10/2013	429.06 429.00	10/2014 10/2015	11/2015	0/0
18	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	06/2012 11/2015	01/2016	0/0
19	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]SPRL,KARNATAKA	01/2006	732.00 1,227.00	10/2011 -	03/2016	0/0
20	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]SPRL,KERALA	01/2006	993.00 1,693.00	01/2012 -	03/2016	0/0
21	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]OCL,GUJARAT	12/2011	160.00 -	02/2016 02/2016	03/2016	0/0
22	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 686.58	04/2015 04/2015	05/2016	0/0
23	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	09/2011 12/2015	06/2016	0/0
24	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]OCL,MULTI STATE	02/2011	913.00 -	08/2015 -	12/2016	0/0
25	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM	03/2009	228.64 -	12/2016 -	12/2016	0/0
26	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	03/2017 -	03/2017	0/0
27	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]OCL,ODISHA	03/2014	238.50 -	03/2017 -	03/2017	0/0
28	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC,MAHARASHTRA	02/2015	2,899.93 -	05/2017 -	05/2017	0/0
29	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]OCL,ODISHA	03/2014	3,150.00 -	09/2017 -	09/2017	0/0
30	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]ONGC,MAHARASHTRA	12/2012	3,513.07 4,619.94	02/2016 12/2017	12/2017	0/0
31	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]OCL,WEST BENGAL	03/2014	3,076.00 -	09/2017 -	12/2017	0/0
32	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA	11/2014	6,068.80 -	04/2019 -	03/2019	0/0
33	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA	08/2015	2,818.88 -	03/2019 -	03/2019	0/0
34	GAMJI REDEVELOPMENT PROJECT - [N16000202]ONGC,GUJARAT	05/2015	1,671.22 1,881.22	11/2019 -	11/2019	0/0

(November 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
35	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI	08/2014	6,086.08 -	05/2019 03/2020	03/2020	0/0
36	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	-	-	0/0
37	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	-	-	0/0
38	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 -	-	-	0/0
39	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00 -	-	-	0/0
40	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE	02/2015	890.00 -	-	-	0/0
	Total		41,392.72 -			0/0
	<u>POWER</u>					
41	BOKARO THERMAL POWER STATION-A - [N18000199]DVC,JHARKHAND	08/2006	2,313.00 4,139.00	12/2011 -	03/2016	0/0
42	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I) - [N18000198]PGCIL,ANDHRA PRADESH	05/2015	312.94 -	05/2016 -	05/2016	0/0
43	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	09/2014 -	06/2016	0/0
44	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	04/2016 -	11/2016	0/0
45	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]DVC,WEST BENGAL	04/2007	4,122.00 8,781.00	02/2011 -	01/2017	0/0
46	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL,DELHI	05/2015	780.33 -	07/2017 -	07/2017	0/0
47	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24 -	09/2017 -	09/2017	0/0
48	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN	07/2015	307.18 -	11/2017 -	11/2017	0/0
49	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	03/2018 -	03/2018	0/0
50	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL,MULTI STATE	07/2015	2,247.37 -	07/2018 -	07/2018	0/0
51	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]NHPC,JAMMU AND KASHMIR	10/2014	8,112.12 -	04/2020 -	04/2020	0/0
52	SUBANSIRI LOWER H.E.P (8x250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-	0/0
	Total		26,322.17 -			0/0
	<u>HEAVY INDUSTRY</u>					
53	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]HIPE,MULTI STATE	04/2011	1,718.00 -	09/2011 -	12/2017	0/0
	Total		1,718.00 -			0/0

(November 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	<u>HEALTH AND FAMILY WELFARE</u>					
54	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	11/2014	0/0
55	AIIMS-RAEBARELI-HOUSING - [N21000006]HSCC,UTTAR PRADESH	10/2013	159.50 -	11/2013 -	09/2015	0/0
56	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK - [N21000004]HSCC,DELHI	09/2013	444.70 -	12/2015 -	12/2015	0/0
57	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT & OTHERS-EMERGENCY BLOCK - [N21000005]HSCC,DELHI	11/2013	196.70 -	01/2016 -	01/2016	0/0
58	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	03/2016	0/0
	Total		1,390.58 -			0/0
	<u>RAILWAYS</u>					
59	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	07/2008	0/0
60	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87 -	- 03/2010	03/2010	0/0
61	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	02/2012	0/0
62	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 663.01	06/1999 -	07/2012	0/0
63	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 03/2012	12/2012	0/0
64	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTT,TAMIL NADU	04/2006	495.74 -	06/2013 06/2013	06/2013	0/0
65	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	611.03 -	12/2011 11/2013	11/2013	0/0
66	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 -	- -	02/2014	0/0
67	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2014	0/0
68	CUTTACK - BARANG (LD) - [220100326]RVNL,ODISHA	04/1995	127.13 -	- 10/2014	10/2014	0/0
69	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	171.02 -	06/2013 -	01/2015	0/0
70	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	96.16 -	- -	01/2015	0/0
71	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	03/1994 -	03/2015	0/0
72	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	02/2009 -	03/2015	0/0
73	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 236.41	- -	03/2015	0/0
74	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 393.46	03/2007 03/2007	03/2015	0/0

(November 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
75	GULBARGA-BIDAR, SCR(NL) - [220100254]SCR, KARNATAKA	02/1998	242.42 369.70	- 05/2009	03/2015	0/0
76	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR, RAJASTHAN	04/2008	829.74 -	03/2015 -	03/2015	0/0
77	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR, TAMIL NADU	04/2007	247.00 -	- -	03/2015	0/0
78	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER, MULTI STATE	04/2011	248.07 -	03/2015 -	03/2015	0/0
79	PEN ROHA DOUBLING - [N22000254]CR, MULTI STATE	04/2007	98.74 -	- -	03/2015	0/0
80	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR, UTTAR PRADESH	04/1999	108.00 427.21	12/2009 03/2011	06/2015	0/0
81	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII-MUSORE (SWR) - [N22000107]SWR, KARNATAKA	04/2007	482.00 -	03/2013 -	09/2015	0/0
82	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL	04/1999	207.52 -	12/2012 -	09/2015	0/0
83	HOSADURGA - CHICKJAJUR (28.89 KM) - [N22000324]SWR, KARNATAKA	04/2010	203.40 -	- -	09/2015	0/0
84	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR, BIHAR	04/2002	921.00 -	03/2009 12/2012	10/2015	0/0
85	ETAWAH-MAINPURI (NL), NCR - [220100318]NCR, UTTAR PRADESH	04/1997	120.00 245.39	12/2008 -	10/2015	0/0
86	RANCHI-LOHARDAGA(GC), SER - [220100214]SER, JHARKHAND	04/1997	194.07 -	06/2004 -	12/2015	0/0
87	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR, BIHAR	04/2001	624.47 -	10/2007 12/2012	12/2015	0/0
88	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, MADHYA PRADESH	09/2007	687.20 -	03/2010 -	12/2015	0/0
89	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP, MAHARASHTRA	03/1996	495.44 495.44	03/2004 -	03/2016	0/0
90	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR, TAMIL NADU	09/2006	343.17 -	- -	03/2016	0/0
91	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE, UTTAR PRADESH	02/2008	171.10 236.37	03/2012 12/2013	03/2016	0/0
92	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	03/2016 -	03/2016	0/0
93	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	03/2016 -	03/2016	0/0
94	KATAKHAL TO BHAIKABI - [N22000126]NFR, ASSAM	04/1998	227.90 200.00	12/2012 -	03/2016	0/0
95	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR, ASSAM	04/1996	1,676.31 -	03/2009 -	03/2016	0/0
96	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER, JHARKHAND	04/2010	309.44 388.67	12/2015 -	03/2016	0/0
97	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR, TRIPURA	04/1999	895.00 575.00	03/2007 -	03/2016	0/0
98	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP, TELANGANA	04/2012	632.68 -	03/2016 -	03/2016	0/0

(November 2015)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
99	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	06/2016	0/0
100	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER, ODISHA	04/2010	149.90 -	03/2015 -	12/2016	0/0
101	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR, ODISHA	03/2012	155.81 -	- -	12/2016	0/0
102	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER, JHARKHAND	04/2012	148.77 -	12/2016 -	12/2016	0/0
103	RAMGANJMUNDI-BHOPAL (NL), WCR - [220100314]WCR, MADHYA PRADESH	04/2001	470.92 727.13	- -	03/2017	0/0
104	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, MADHYA PRADESH	04/2005	383.79 663.67	- -	03/2017	0/0
105	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	200.00 200.00	- -	03/2017	0/0
106	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR, UTTAR PRADESH	04/2006	325.00 -	03/2010 03/2017	03/2017	0/0
107	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR, MULTI STATE	04/2010	241.52 210.00	- -	03/2017	0/0
108	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	03/2017	0/0
109	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER, MULTI STATE	04/2011	299.60 -	03/2017 -	03/2017	0/0
110	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER, MULTI STATE	04/2010	423.66 -	03/2017 -	03/2017	0/0
111	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR, ASSAM	09/1997	1,500.00 1,000.00	04/2008 03/2014	06/2017	0/0
112	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER, JHARKHAND	04/2012	258.20 315.13	- -	12/2017	0/0
113	KANPUR-KASGANJ-MATHURA(GC), NER - [220100197]NER, UTTAR PRADESH	03/1997	677.97 1,062.36	- -	03/2018	0/0
114	KATI HAR - JOGBANI (GC)(NEFR) - [220100247]NFR, BIHAR	09/2001	492.98 -	12/2010 -	03/2018	0/0
115	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	733.00 733.00	12/2008 -	03/2018	0/0
116	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA	04/2008	813.34 813.34	03/2014 -	03/2018	0/0
117	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	619.34 619.34	04/2014 03/2015	03/2018	0/0
118	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR, BIHAR	04/2008	282.92 282.92	- 03/2014	03/2018	0/0
119	AGARTALA-AKHAURA NL - [N22000195]NFR, TRIPURA	04/2012	252.00 -	- -	03/2018	0/0
120	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR, WEST BENGAL	04/2011	209.77 190.39	- -	03/2018	0/0
121	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR, WEST BENGAL	04/2012	283.55 278.21	- -	03/2018	0/0
122	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR, MULTI STATE	04/2010	242.22 171.00	- -	03/2018	0/0

(November 2015)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
123	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	165.82 165.82	- -	03/2018	0/0
124	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NFR,MULTI STATE	04/1999	523.17 380.60	- -	03/2018	0/0
125	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	312.12 257.93	- -	03/2018	0/0
126	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 -	- -	03/2018	0/0
127	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	06/2018	0/0
128	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	11/2002 -	12/2018	0/0
129	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 2,030.50	02/2019 -	02/2019	0/0
130	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR, WEST BENGAL	04/1983	36.80 36.38	- -	03/2019	0/0
131	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 727.56	03/2011 03/2014	03/2019	0/0
132	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	300.00 300.00	- -	03/2019	0/0
133	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 6,821.29	03/2014 03/2019	03/2019	0/0
134	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 1,798.00	- -	03/2019	0/0
135	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 205.31	- -	03/2019	0/0
136	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM	04/2012	246.07 246.07	- -	03/2019	0/0
137	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,157.54	03/1998 -	12/2019	0/0
138	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	03/2005 12/2008	12/2019	0/0
139	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97 1,013.74	06/2005 07/2011	12/2019	0/0
140	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 651.17	- -	12/2019	0/0
141	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 3,845.60	02/2020 -	02/2020	0/0
142	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 1,339.48	12/2015 -	03/2020	0/0
143	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00 -	03/2015 03/2020	03/2020	0/0
144	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	- -	03/2020	0/0
145	NEW BG LINE FROM BYRNIAHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	4,083.02 -	- 03/2016	03/2020	0/0
146	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	02/2009 02/2009	-	0/0

(November 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
147	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 -	- 03/2010	-	0/0
148	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-	0/0
149	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	12/2011 12/2010	-	0/0
150	AHMEDNAGAR-PARLI VAJUNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	- -	-	0/0
151	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 -	- -	-	0/0
152	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	- -	-	0/0
153	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-	0/0
154	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-	0/0
155	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	- -	-	0/0
156	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	2,957.21 -	07/2005 -	-	0/0
157	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	05/2008 -	-	0/0
158	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 501.69	03/2012 -	-	0/0
159	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	- -	-	0/0
160	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-	0/0
161	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-	0/0
162	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 -	- -	-	0/0
163	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	- -	-	0/0
164	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 3,385.14	12/2006 -	-	0/0
165	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	02/2011 02/2011	-	0/0
166	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	- 12/2009	-	0/0
167	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-	0/0
168	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 -	- -	-	0/0
169	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	- -	-	0/0
170	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	- 09/2009	-	0/0

(November 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
171	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-	0/0
172	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-	0/0
173	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-	0/0
174	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-	0/0
175	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	- -	-	0/0
176	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	- -	-	0/0
177	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	02/2015 -	-	0/0
178	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	03/2009 03/2009	-	0/0
179	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	- -	-	0/0
180	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-	0/0
181	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 332.92	03/2012 -	-	0/0
182	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	378.56 -	- -	-	0/0
183	GOELKERA-MANOHPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	261.70 -	02/2006 -	-	0/0
184	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-	0/0
185	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	03/2010 -	-	0/0
186	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	- -	-	0/0
187	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE	12/2006	170.00 -	03/2011 -	-	0/0
188	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 -	- -	-	0/0
189	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 -	- -	-	0/0
190	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	1,106.62 -	12/2010 -	-	0/0
191	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	03/2014 -	-	0/0
192	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	03/2014 -	-	0/0
193	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 732.06	03/2014 -	-	0/0
194	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	-	0/0

(November 2015)						
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
195	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	533.38 -	12/2011 -	-	0/0
196	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	293.74 -	12/2010 -	-	0/0
197	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR, MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-	0/0
198	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR, GUJARAT	04/2008	394.14 -	03/2013 -	-	0/0
199	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR, GUJARAT	04/2008	1,389.62 -	03/2014 -	-	0/0
200	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR, GUJARAT	04/2008	318.24 -	03/2012 -	-	0/0
201	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR, GUJARAT	04/2006	117.36 196.95	03/2011 -	-	0/0
202	ANANDNAGAR GHUGHALI VIA MAHARAJGANJ UP - [N22000130]NER, UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0
203	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER, MULTI STATE	03/2007	243.78 -	- -	-	0/0
204	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER, UTTAR PRADESH	03/2008	195.64 -	- -	-	0/0
205	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER, UTTAR PRADESH	03/2012	199.75 -	- -	-	0/0
206	CHHAPRA-BALLIA UP - [N22000134]NER, MULTI STATE	03/2013	295.00 -	- -	-	0/0
207	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER, UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
208	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR, RAJASTHAN	04/2012	246.08 -	- -	-	0/0
209	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR, MULTI STATE	04/2007	1,347.26 -	- -	-	0/0
210	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR, MULTI STATE	04/2007	1,640.04 -	- -	-	0/0
211	AHMEDABAD-BOTAD (GC) - [N22000140]WR, GUJARAT	04/2012	567.18 -	- -	-	0/0
212	DHASA-JETALSAR (GC) - [N22000141]WR, GUJARAT	04/2012	376.59 -	- -	-	0/0
213	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR, GUJARAT	04/2011	439.88 -	- -	-	0/0
214	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR, GUJARAT	04/1994	320.66 913.48	- -	-	0/0
215	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR, GUJARAT	04/2013	1,266.89 -	- -	-	0/0
216	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR, GUJARAT	04/2011	446.00 -	- -	-	0/0
217	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR, GUJARAT	04/2010	279.40 -	- -	-	0/0
218	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR, MULTI STATE	04/2011	2,082.75 -	- -	-	0/0

(November 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
219	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	-	0/0
220	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-	0/0
221	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0
222	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	- -	-	0/0
223	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	- -	-	0/0
224	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	- -	-	0/0
225	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	- -	-	0/0
226	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	- -	-	0/0
227	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	- -	-	0/0
228	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	- -	-	0/0
229	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL	04/2011	289.64 -	- -	-	0/0
230	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	- -	-	0/0
231	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-	0/0
232	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-	0/0
233	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-	0/0
234	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-	0/0
235	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-	0/0
236	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-	0/0
237	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-	0/0
238	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-	0/0
239	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-	0/0
240	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-	0/0
241	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-	0/0
242	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-	0/0

(November 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
243	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-	0/0
244	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-	0/0
245	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-	0/0
246	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-	0/0
247	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	- -	-	0/0
248	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-	0/0
249	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-	0/0
250	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-	0/0
251	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-	0/0
252	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	- -	-	0/0
253	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-	0/0
254	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-	0/0
255	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-	0/0
256	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-	0/0
257	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-	0/0
258	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-	0/0
259	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSHPUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-	0/0
260	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-	0/0
261	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	- -	-	0/0
262	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-	0/0
263	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-	0/0
264	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-	0/0
265	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-	0/0
266	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-	0/0

(November 2015)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
267	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-	0/0
268	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-	0/0
269	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-	0/0
270	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-	0/0
271	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-	0/0
272	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-	0/0
273	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-	0/0
274	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	- -	-	0/0
275	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-	0/0
276	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-	0/0
277	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-	0/0
278	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-	0/0
279	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-	0/0
280	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-	0/0
281	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-	0/0
282	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-	0/0
283	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-	0/0
284	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-	0/0
285	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	- -	-	0/0
286	SANTOSHUPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-	0/0
287	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-	0/0
288	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-	0/0
289	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-	0/0
290	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-	0/0

(November 2015)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
291	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93	-	-	0/0
292	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00	-	-	0/0
293	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE	04/2013	723.00	-	-	0/0
294	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35	-	-	0/0
295	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE	04/2008	184.26	-	-	0/0
296	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23	-	-	0/0
297	GUDUR-DURGARAJPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54	-	-	0/0
298	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44	-	-	0/0
299	MANSABHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04	-	-	0/0
300	GRADE SEPARATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65	-	-	0/0
301	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00	-	-	0/0
302	DELHI-SOHNANUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00	-	-	0/0
303	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00	-	-	0/0
304	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88	-	-	0/0
305	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91	-	-	0/0
306	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00	-	-	0/0
307	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00	-	-	0/0
308	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74	-	-	0/0
309	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34	-	-	0/0
310	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05	-	-	0/0
311	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68	-	-	0/0
312	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00	-	-	0/0
313	MUDKHED-PARBHANI - [N22000283]SCR,MAHARASHTRA	04/2011	390.60	-	-	0/0
314	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48	-	-	0/0

(November 2015)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
315	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49 -	- -	-	0/0
316	KADAPA-BANGALORE (NL), KADAPA-PENDIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	- -	-	0/0
317	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-	0/0
318	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-	0/0
319	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-	0/0
320	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-	0/0
321	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-	0/0
322	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-	0/0
323	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-	0/0
324	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-	0/0
325	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	- -	-	0/0
326	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-	0/0
327	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	- -	-	0/0
328	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	-	0/0
329	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-	0/0
330	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-	0/0
331	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	01/1999 -	-	0/0
332	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 -	-	0/0
333	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-	0/0
334	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	01/1999 -	-	0/0
335	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-	0/0
336	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	- -	-	0/0
337	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 -	- -	-	0/0
338	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 -	- -	-	0/0

(November 2015)						
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
339	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	- -	-	0/0
340	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	03/2015 -	03/2015	0/0
341	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-	0/0
342	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR,TAMIL NADU	04/2011	190.10 -	- -	-	0/0
343	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,900.00 -	- -	-	0/0
344	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	- -	-	0/0
345	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 -	- -	-	0/0
346	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	- -	-	0/0
347	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-	0/0
348	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-	0/0
349	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA	05/2015	400.00 -	- -	-	0/0
350	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA	03/2015	960.00 -	- -	-	0/0
351	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 -	- -	-	0/0
352	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	720.00 -	- -	-	0/0
	Total		170,856.70 -			0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
353	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH	12/2014	201.12 201.00	02/2015 -	02/2015	0/0
354	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA	10/2013	283.25 -	10/2015 -	10/2015	0/0
355	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	11/2015 -	11/2015	0/0
356	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	04/2008 12/2015	12/2015	0/0
357	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	04/2008 12/2015	12/2015	0/0
358	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 12/2015	12/2015	0/0
359	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR - [N24000238]NHAI,RAJASTHAN	01/2014	158.04 -	12/2015 -	12/2015	0/0
360	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD,TELANGANA	03/2011	218.31 -	12/2015 -	12/2015	0/0

(November 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
361	2-LANING WITH PS OF JHALAWAR-RAJASTHAN-MP. BORDER - [N24000237]NHAI,RAJASTHAN	01/2014	177.32 -	01/2016 -	01/2016	0/0
362	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANAMERTA CITY SECTION - [N24000239]NHAI,RAJASTHAN	01/2014	368.15 -	01/2016 -	01/2016	0/0
363	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	04/2010 02/2016	02/2016	0/0
364	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI,RAJASTHAN	03/2014	240.10 -	03/2016 -	03/2016	0/0
365	YAN TO NIRMAL SEREHAHABILITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA	12/2013	244.08 -	03/2016 -	03/2016	0/0
366	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD,TELANGANA	01/2014	340.00 -	03/2016 -	03/2016	0/0
367	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]PWD,TELANGANA	01/2014	270.00 -	03/2016 -	03/2016	0/0
368	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 04/2016	04/2016	0/0
369	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 04/2016	04/2016	0/0
370	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236]NHAI,RAJASTHAN	10/2013	677.79 -	04/2016 -	04/2016	0/0
371	CONSTRUCTION OF MAJOR/MINOR BRIDGE & ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO 45 - [N24000253]NHDP,MAHARASHTRA	08/2014	187.79 -	07/2016 -	07/2016	0/0
372	REHABILITATION & UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) T - [N24000267]PWD,ANDHRA PRADESH	02/2014	258.99 -	07/2014 -	07/2016	0/0
373	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	09/2016 -	09/2016	0/0
374	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	11/2016	0/0
375	REHABILITATION & UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]NHDP,MAHARASHTRA	06/2014	260.39 -	11/2016 -	11/2016	0/0
376	REHABILITATION & UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]NHDP,MAHARASHTRA	12/2013	220.72 -	11/2016 -	11/2016	0/0
377	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]PWD,TELANGANA	10/2014	244.30 -	12/2016 -	12/2016	0/0
378	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	04/2008 01/2017	01/2017	0/0
379	EPC- CORRIDOR APPROACH WORKS - NH (O); WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA	03/2015	153.21 -	01/2017 -	01/2017	0/0
380	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAPUR - [N24000247]PWD,TELANGANA	10/2014	295.47 -	02/2017 -	02/2017	0/0
381	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]PWD,ANDHRA PRADESH	02/2015	241.61 -	02/2017 -	02/2017	0/0
382	REHABILITATION & UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN T - [N24000265]PWD,ANDHRA PRADESH	11/2014	297.78 330.00	02/2017 -	02/2017	0/0
383	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH	07/2014	251.55 -	02/2015 -	02/2017	0/0
384	REHABILITATION & UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA	01/2014	446.77 -	- -	06/2017	0/0

(November 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
385	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA	01/2014	255.75 348.00	09/2017 -	09/2017	0/0
386	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDEAPAR BRIDGE - [N24000251]NHDP,GOA	03/2015	297.00 -	- -	10/2017	0/0
387	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA	03/2015	168.30 -	- -	10/2017	0/0
388	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA	01/2014	267.16 352.00	11/2017 -	11/2017	0/0
389	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 -	09/2007 -	-	0/0
390	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	09/2008 -	-	0/0
391	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	06/2005 -	-	0/0
392	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	10/2008 -	-	0/0
393	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	-	0/0
394	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	-	0/0
395	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	-	0/0
396	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-	0/0
397	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	04/2009 -	-	0/0
398	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	06/2008 -	-	0/0
399	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	06/2008 -	-	0/0
400	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	09/2008 -	-	0/0
401	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	10/2008 -	-	0/0
402	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	10/2008 -	-	0/0
403	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	07/2008 -	-	0/0
404	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-	0/0
405	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	06/2008 -	-	0/0
406	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-	0/0
407	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 -	09/2007 -	-	0/0
408	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	-	0/0

(November 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
409	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	02/2010 -	-	0/0
410	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-	0/0
411	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	09/2007 -	-	0/0
412	NH CONNECTIVITY TO ICTT VALLARPADAUE NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	02/2010 -	-	0/0
413	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	09/2010 -	-	0/0
414	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	-	0/0
415	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	07/2012 -	-	0/0
416	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	05/2012 -	-	0/0
417	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	10/2011 -	-	0/0
418	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	10/2011 -	-	0/0
419	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	-	0/0
420	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	12/2012 -	-	0/0
421	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	-	0/0
422	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	09/2013 -	-	0/0
423	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	-	0/0
424	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	01/2013 -	-	0/0
425	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA	02/2010	390.56 -	02/2012 -	-	0/0
426	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	03/2013 -	-	0/0
427	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	-	0/0
428	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	07/2013 -	-	0/0
429	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	-	0/0
430	WADNER-DEVDHARI(NS-60/MH)/(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	11/2012 -	-	0/0
431	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00 -	10/2014 -	-	0/0
432	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	09/2013 -	-	0/0

(November 2015)						
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
433	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	06/2013 -	-	0/0
434	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-	0/0
435	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	-	0/0
436	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-	0/0
437	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	-	0/0
438	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-	0/0
439	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-	0/0
440	PATNA-MUZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	-	0/0
441	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	-	0/0
442	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	-	0/0
443	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-	0/0
444	SIX LANNING OF HOSUR- KRISHNAGIRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	12/2013 -	-	0/0
445	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	-	0/0
446	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	-	0/0
447	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	-	0/0
448	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	-	0/0
449	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	-	0/0
450	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-	0/0
451	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	03/2013 -	-	0/0
452	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	01/2014 -	-	0/0
453	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	02/2014 -	-	0/0
454	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014 -	-	0/0
455	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	-	0/0
456	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	02/2014 -	-	0/0

(November 2015)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
457	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	-	0/0
458	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-	0/0
459	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	-	0/0
460	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	-	0/0
461	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	-	0/0
462	2LANING WITH PS GOPALGANJ-CHAPPRA - [N24000190]NHAI,BIHAR	12/2011	325.00 -	05/2014 -	-	0/0
463	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	02/2014 -	-	0/0
464	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	01/2013 -	-	0/0
465	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	01/2014 -	-	0/0
466	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	01/2014 -	-	0/0
467	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	08/2013 -	-	0/0
468	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	05/2014 -	-	0/0
469	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	-	0/0
470	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	02/2013 -	-	0/0
471	BEAWARE-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	06/2014 -	-	0/0
472	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	-	0/0
473	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	-	0/0
474	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	08/2013 -	-	0/0
475	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	08/2013 -	-	0/0
476	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	08/2013 -	-	0/0
477	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	06/2014 -	-	0/0
478	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	-	0/0
479	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	07/2012 -	-	0/0
480	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	-	0/0

(November 2015)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
481	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL	02/2012	702.16	07/2014	-	0/0
482	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI, MAHARASHTRA	04/2012	484.19	10/2014	-	0/0
483	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI, BIHAR	07/2012	356.40	07/2014	-	0/0
484	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI, UTTARAKHAND	11/2011	478.00	10/2013	-	0/0
485	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI, MULTI STATE	04/2012	624.00	04/2014	-	0/0
486	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI, KERALA	04/2011	682.00	10/2013	-	0/0
487	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI, MULTI STATE	12/2012	1,479.00	06/2015	-	0/0
488	PANVEL-INDAPUR - [N24000216]NHAI, MULTI STATE	12/2011	942.69	06/2014	-	0/0
489	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI, MULTI STATE	02/2013	1,232.00	08/2015	-	0/0
490	ETAWAH CHAKERI - [N24000219]NHAI, UTTAR PRADESH	03/2013	1,573.00	09/2015	-	0/0
491	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI, UTTAR PRADESH	10/2012	250.50	10/2014	-	0/0
492	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI, UTTAR PRADESH	01/2013	373.47	07/2014	-	0/0
493	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI, MULTI STATE	10/2012	1,928.22	04/2015	-	0/0
494	REENGUS SIKAR - [N24000227]NHAI, RAJASTHAN	03/2012	333.51	09/2014	-	0/0
495	BARSAT-KRISHNANAGAR - [N24000229]NHAI, WEST BENGAL	08/2012	867.00	02/2015	-	0/0
496	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI, MAHARASHTRA	05/2013	1,348.20	02/2014	-	0/0
497	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI, ANDHRA PRADESH	09/2013	606.00	-	-	0/0
498	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI, TELANGANA	04/2014	1,123.17	-	-	0/0
499	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH, GOA	03/2015	298.33	-	-	0/0
500	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD TO FO - [N24000258]DORTH, GOA	03/2015	184.05	-	-	0/0
501	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH, GOA	03/2015	280.16	-	-	0/0
502	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD, ANDHRA PRADESH	03/2015	175.03	-	-	0/0
	Total		94,929.08			0/0
	SHIPPING AND PORTS					

(November 2015)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
503	ACQUISITION OF TWO (2) NOS OF 317000 DWT VLCC'S FROM JIANGSU RONGSHENG HEAVY INDUSTRIES CO.LTD.,CHIN - [N25000064]SHIPP.,MAHARASHTRA	10/2010	994.82 -	11/2013 -	11/2013	0/0
504	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	03/2006 -	12/2015	0/0
505	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 669.46	12/2010 -	01/2016	0/0
506	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 373.22	04/2009 03/2010	08/2016	0/0
507	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 -	12/2010 -	09/2017	0/0
508	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-	0/0
	Total		5,412.28 -			0/0
	<u>TELECOMMUNICATIONS</u>					
509	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	10/2010 08/2015	11/2015	0/0
510	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	07/2015 -	-	0/0
	Total		13,718.00 -			0/0
	<u>URBAN DEVELOPMENT</u>					
511	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB	02/2014	388.00 -	01/2015 -	01/2015	0/0
512	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD,WEST BENGAL	01/2009	225.81 -	06/2012 12/2015	12/2015	0/0
513	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	12/2015	0/0
514	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	08/2014 -	01/2016	0/0
515	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	11/2014 -	03/2016	0/0
516	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI	05/2012	405.01 -	12/2014 -	04/2016	0/0
517	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85 -	05/2013 10/2015	06/2016	0/0
518	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	03/2016 -	12/2016	0/0
519	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	12/2014 -	12/2016	0/0
520	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	09/2015 07/2016	12/2016	0/0
521	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	09/2016 01/2017	01/2017	0/0

(November 2015)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
522	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH	06/2014	157.84 -	03/2017 -	03/2017	0/0
523	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	07/2017 -	07/2017	0/0
524	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	07/2017 -	07/2017	0/0
525	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	03/2018	0/0
526	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	02/2019 -	02/2019	0/0
527	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CENTRA - [N28000089]CPWD,TAMIL NADU	12/2015	209.00 -	- -	-	0/0
528	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]CPWD,BIHAR	02/2012	171.10 -	09/2014 -	-	0/0
529	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI - [N28000064]CPWD,DELHI	01/2010	162.90 -	07/2012 -	-	0/0
530	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD,ODISHA	11/2012	238.43 -	02/2015 -	-	0/0
531	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 -	11/2014 -	-	0/0
532	CONSTRUCTION OF MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB - [N28000070]CPWD,PUNJAB	08/2005	191.24 -	08/2007 -	-	0/0
533	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	03/2012 -	-	0/0
534	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASHTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 -	06/2015 -	-	0/0
535	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	10/2012 -	-	0/0
536	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA - [N28000078]CPWD,BIHAR	11/2006	2,727.89 -	03/2010 -	-	0/0
537	REHABILITATION AND STRENGTHENING OF SEWETRAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI(IN ZONE 2 IN - [N28000082]JnNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-	0/0
	Total		111,352.96 -			0/0
	Grand Total		482,794.78			0/0

List of Projects Ahead of Schedule w.r.t. Latest Schedule

						(November 2015)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
1	NIGAMI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 486.57	486.57	59.23	03/2012 03/2018	03/2017
	Total		259.40 -	486.57	59.23		
	<u>POWER</u>						
2	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]	2/2014	243.53 -	243.53	185.63	08/2016 -	12/2015
3	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW [N18000203]	2/2015	302.49 -	302.49	147.75	02/2016 -	12/2015
	Total		546.02 -	546.02	333.38		
	<u>COAL</u>						
4	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	3.52	03/2021 -	03/2017
	Total		555.52 -	555.52	3.52		
	<u>POWER</u>						
5	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. [N18000170]	8/2014	188.75 -	188.75	70.77	02/2017 -	03/2016
	Total		188.75 -	188.75	70.77		
	<u>PETROLEUM</u>						
6	MARKETING TOP AT KORBA - [N16000186]	1/2011	141.86 -	232.00	159.09	09/2016 -	03/2016
7	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]	7/2014	419.04 -	419.04	240.86	01/2017 -	06/2016
8	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]	11/2014	6,068.80 -	6,068.80	523.70	04/2019 -	03/2019
	Total		6,629.70 -	6,719.84	923.65		
	<u>POWER</u>						
9	SYSTEM STRENGTHENING XIII OF SR GRID [N18000109]	10/2011	487.49 639.46	639.46	412.96	06/2014 03/2016	11/2015
	Total		487.49 -	639.46	412.96		

(November 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	Grand Total		8,666.88	9,136.16	1,803.51		

List of Projects on schedule w.r.t. Latest Schedule

(November 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
1	AMRITDHARA OC PROJECT - [N06000122	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
2	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129	5/2015	397.09 -	397.09	-	03/2019 -	03/2019
3	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112	5/2014	479.15 -	479.15	10.25	03/2019 -	03/2019
4	RAMPUR BATURA OCP (4.0 MTY) - [N06000049	8/2015	1,186.64 -	1,186.64	1.33	03/2023 -	03/2023
5	GOKUL - [N06000120	11/2014	267.67 -	267.67	176.11	03/2018 -	03/2018
6	AMERA OC RCE - [N06000123	2/2015	335.97 -	335.97	30.90	03/2018 -	03/2018
7	GARJANBAHAL OCP - [N06000117	11/2014	1,375.38 -	1,375.38	158.45	03/2021 -	03/2021
8	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124	12/2014	357.80 -	357.80	108.44	03/2021 -	03/2021
9	CHHAL OC SEAM -III (6.00 MTY) - [N06000104	12/2013	610.63 -	610.33	-	03/2022 -	03/2022
10	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008	8/2013	7,612.33 -	7,612.33	783.81	03/2023 03/2023	03/2023
11	PELMA OCP(15.00MTY) - [N06000045	11/2014	1,624.59 -	1,624.59	5.43	03/2023 03/2023	03/2023
12	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114	5/2014	337.66 -	337.66	0.29	03/2019 -	03/2019
13	KANCHAN OC EXPANSION - [N06000125	12/2014	371.04 -	371.04	28.78	03/2021 -	03/2021
14	SIARMAL OCP (40.00MTY) - [N06000113	5/2014	3,756.36 -	3,756.36	620.40	03/2026 -	03/2026
15	BIJARI OC RCE (1.50 MTY) - [N06000111	5/2014	164.49 -	164.49	76.43	03/2020 -	03/2020
16	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091	6/2011	1,131.28 -	1,131.28	125.67	03/2018 -	03/2018
17	AMALGAMATED YEKONA-I YEKONA-II - [N06000132	8/2015	727.28 -	727.28	51.53	03/2025 -	03/2025
18	BHANEGAON OC - [N06000121	2/2015	187.94 -	187.94	46.65	03/2023 -	03/2023
19	AMALGAMATED PAUNI-II III OC MINE - [N06000131	6/2015	483.69 -	483.69	31.57	03/2021 -	03/2021
20	DINESH OCP - [N06000118	11/2014	611.16 -	611.16	116.97	03/2020 -	03/2020
21	AMGAON OPENCAST PROJECT RCE - [N06000135	7/2015	316.10 -	316.10	15.85	03/2020 -	03/2020

(November 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
22	KAPURIA UG(PSLW) - [N06000108]	8/2011	988.35 -	988.35	45.27	04/2017 -	04/2017
23	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	92.30	03/2021 -	03/2021
24	MOONIDIH XV SEAM UG - [N06000098]	8/2011	1,230.27 -	1,230.27	47.76	04/2015 04/2019	04/2019
25	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]	8/2012	1,055.05 -	1,055.05	191.06	03/2018 -	03/2018
26	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	6/2011	5,907.11 -	5,907.11	1,204.77	12/2015 04/2018	04/2018
27	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	122.91	03/2016 -	03/2016
28	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	-	03/2023 -	03/2023
29	KULDA EXPN OC. (5.00 MTY) - [N06000115]	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
30	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]	12/2009	1,352.04 -	1,143.54	808.39	03/2016 -	03/2016
31	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
32	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	295.56	79.02	03/2019 -	03/2019
33	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	127.86	03/2020 -	03/2020
34	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	486.27	93.51	03/2016 -	03/2016
35	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	108.17	03/2020 -	03/2020
36	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.10 -	490.10	203.58	03/2017 -	03/2017
37	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]	12/2009	510.85 -	510.85	224.44	03/2016 -	03/2016
38	ADASA UG TO OC - [N06000133]	8/2015	288.90 -	288.90	-	03/2023 -	03/2023
	Total		38,518.47 -	38,413.49	5,737.90		
	FERTILISERS						
39	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	197.79	37.66	11/2016 -	11/2016
	Total		197.79 -	197.79	37.66		
	HEALTH AND FAMILY WELFARE						
40	SAFDARJUNG HOSPITAL, NEW DELHI- REDEVELOPMENT & OTHERS-EMERGENCY BLOCK - [N21000005]	11/2013	196.70 -	196.70	-	01/2016 -	01/2016

							(November 2015)	
						Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated	
1	2	3	4	5	6	7	8	
41	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK - [N21000004	9/2013	444.70 -	444.70	228.19	12/2015 -	12/2015	
	Total		641.40 -	641.40	228.19			
	<u>MINES</u>							
42	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007	9/2011	1,856.00 -	1,856.00	-	09/2017 -	09/2017	
	Total		1,856.00 -	1,856.00	.00			
	<u>PETROLEUM</u>							
43	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131	12/2011	2,059.63 -	2,665.65	1,282.07	03/2015 05/2016	05/2016	
44	DAMAN DEVELOPMENT PROJECT - [N16000198	8/2014	6,086.08 -	6,086.08	586.87	05/2019 03/2020	03/2020	
45	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204	8/2015	2,818.88 -	2,818.88	-	03/2019 -	03/2019	
46	TWENTY NOS. FEEDER GAS LINES - [N16000192	3/2009	228.64 -	214.19	135.00	12/2016 -	12/2016	
47	IOR OF B-173A FIELD - [N16000140	1/2012	352.49 -	352.49	131.19	03/2014 05/2016	05/2016	
48	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183	3/2014	2,476.82 -	2,476.82	368.95	12/2018 -	12/2018	
49	MH NORTH REDEVELOPMENT PHASE III - [N16000188	6/2014	5,706.47 -	5,813.25	2,268.83	05/2017 05/2017	05/2017	
50	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105	6/2010	2,523.00 -	2,523.00	1,658.41	01/2014 12/2015	12/2015	
51	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133	3/2012	2,592.17 -	2,592.17	826.62	05/2014 05/2016	05/2016	
52	PARADIP LPG IMPORT FACILITY - [N16000196	1/2015	690.00 -	690.00	15.00	07/2018 -	07/2018	
53	RESID UPGRADATION PROJECT - [N16000184	2/2011	3,110.36 -	3,110.36	1,211.76	11/2015 07/2016	07/2016	
54	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167	7/2011	352.56 -	450.55	10.60	03/2017 -	03/2017	
55	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201	3/2014	238.50 -	238.50	1.07	03/2017 -	03/2017	
56	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179	3/2014	3,150.00 -	3,150.00	110.77	09/2017 -	09/2017	
57	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146	2/2012	666.00 -	838.08	546.07	11/2015 11/2016	11/2016	
58	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180	2/2014	163.88 -	163.88	46.91	07/2016 -	07/2016	

						(November 2015)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
59	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]	5/2015	257.87 -	257.87	33.94	11/2016 -	11/2016
60	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]	9/2011	202.25 -	160.16	68.96	07/2016 -	07/2016
61	GAMJI REDEVELOPMENT PROJECT - [N16000202]	5/2015	1,671.22 -	1,881.22	-	11/2019 -	11/2019
62	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]	12/2012	3,513.07 -	4,619.94	667.40	02/2016 12/2017	12/2017
63	MARKETING TERMINAL AT PARADEEP - [N16000168]	7/2009	199.75 -	239.73	205.75	07/2013 11/2015	11/2015
64	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79	253.37	10/2014 03/2017	03/2017
65	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	5/2013	4,124.35 -	4,941.49	521.23	04/2016 12/2017	12/2017
66	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	59.42	10/2017 10/2017	10/2017
67	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]	2/2015	2,899.93 -	2,899.93	502.37	05/2017 -	05/2017
68	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]	4/2013	284.82 -	284.82	-	04/2015 05/2017	05/2017
69	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	3/2012	14,225.00 -	16,504.00	9,087.43	05/2016 -	05/2016
70	REWARI KANPUR PIPELINE PROJECT - [N16000145]	2/2012	1,210.64 -	1,446.34	1,249.03	11/2015 -	11/2015
	Total		62,721.25 -	68,596.44	21,849.02		
	POWER						
71	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	142.00	08/2017 -	08/2017
72	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	12,532.44	2,151.00	08/2018 -	08/2018
73	FGUTPP, UNCHAHAH STAGE-IV (1X500 MW) - [N18000174]	7/2013	3,363.12 -	3,363.12	882.00	12/2016 -	12/2016
74	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	1/2013	12,964.60 -	12,964.60	4,609.32	01/2018 -	01/2018
75	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	1/2015	203.28 -	203.28	18.38	07/2017 -	07/2017
76	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]	3/2015	197.40 -	197.40	-	03/2018 -	03/2018
77	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]	5/2015	780.33 -	780.33	-	07/2017 -	07/2017
78	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	2/2009	11,130.19 -	13,762.80	11,184.10	08/2013 12/2017	12/2017

(November 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
79	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]	10/2014	8,112.12 -	8,112.12	-	04/2020 -	04/2020
80	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]	8/2014	288.49 -	288.49	48.40	02/2017 -	02/2017
81	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,487.49	1,074.08	08/2013 05/2016	05/2016
82	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]	9/2013	680.69 -	680.69	421.64	03/2016 -	03/2016
83	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58 -	14,366.58	2,241.00	02/2019 -	02/2019
84	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]	5/2014	829.98 -	829.98	64.00	08/2016 -	08/2016
85	MOUDA STPP STAGE 2 - [N18000132]	3/2012	7,921.47 -	7,921.47	4,704.00	09/2016 -	09/2016
86	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]	12/2014	6,517.36 -	6,517.36	231.99	04/2018 -	04/2018
87	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]	4/2015	3,705.61 -	3,705.61	138.53	04/2018 -	04/2018
88	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I) - [N18000198]	5/2015	312.94 -	312.94	2.11	05/2016 -	05/2016
89	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]	4/2015	1,479.30 -	1,479.30	60.62	04/2017 -	04/2017
90	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]	3/2015	1,394.52 -	1,394.52	-	05/2017 -	05/2017
91	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]	3/2015	1,071.24 -	1,071.24	-	09/2017 -	09/2017
92	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]	3/2014	155.57 -	155.57	1.00	03/2016 -	03/2016
93	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 -	522.29	47.20	11/2016 -	11/2016
94	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]	9/2013	1,575.30 -	1,575.30	623.05	05/2016 -	05/2016
95	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,476.34	4,252.71	12/2009 12/2016	12/2016
96	WARDHA-HYDERABAD 765 KV LINK - [N18000183]	1/2015	3,662.02 -	3,662.02	295.06	05/2018 -	05/2018
97	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	2/2014	908.08 -	908.08	114.91	06/2016 -	06/2016
98	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]	3/2015	550.06 -	550.06	1.60	03/2018 -	03/2018

(November 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
99	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	891.00	03/2019 -	03/2019
100	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]	2/2014	378.71 -	378.71	113.06	10/2016 -	10/2016
101	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]	1/2015	268.80 -	268.80	20.32	03/2018 -	03/2018
102	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	11,638.55	4,480.00	09/2017 -	09/2017
103	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.84	149.00	09/2019 -	09/2019
104	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]	5/2014	303.07 -	303.07	19.70	07/2016 -	07/2016
105	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]	2/2014	539.82 -	539.82	100.76	06/2016 -	06/2016
106	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]	1/2015	871.62 -	871.62	1.90	10/2017 -	10/2017
107	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	7/1998	368.72 -	1,381.71	910.21	07/2006 10/2017	10/2017
108	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]	6/2014	400.47 -	400.47	45.19	04/2017 -	04/2017
109	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,364.52	430.87	04/2016 -	04/2016
110	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]	7/2015	2,247.37 -	2,247.37	15.10	07/2018 -	07/2018
111	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	11,846.00	5,137.00	06/2017 -	06/2017
112	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]	11/2014	972.42 -	972.42	-	11/2017 -	11/2017
113	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]	2/2014	167.40 -	167.40	84.40	12/2015 -	12/2015
114	TRIPURA GAS BASED POWER PROJECT - [N18000071]	7/2009	421.01 -	1,007.57	947.62	07/2013 12/2015	12/2015
115	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]	5/2015	436.68 -	436.68	398.45	12/2016 -	12/2016
116	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]	7/2015	307.18 -	307.18	0.80	11/2017 -	11/2017
117	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPSPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	702.99	03/2018 -	03/2018
	Total		148,077.40 -	157,202.50	47,757.07		

(November 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	RAILWAYS						
118	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]	4/2010	622.41 -	2,030.50	3.61	02/2019 -	02/2019
119	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	4/2011	299.60 -	299.60	-	03/2017 -	03/2017
120	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	4/2012	632.68 -	816.55	48.00	03/2016 -	03/2016
121	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	4/2008	5,300.00 -	7,986.04	2,443.62	03/2014 03/2019	03/2019
122	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	1,176.09 -	3,845.60	2.33	02/2020 -	02/2020
123	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	4/2010	2,913.51 -	2,619.02	545.87	03/2016 -	03/2016
124	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	4/2006	325.00 -	1,564.54	420.71	03/2010 03/2017	03/2017
125	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	4/2010	3,951.98 -	3,951.98	664.51	03/2016 -	03/2016
126	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	4/2012	148.77 -	209.00	2.64	12/2016 -	12/2016
127	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	4/2010	423.66 -	423.66	163.59	03/2017 -	03/2017
128	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	4/2006	850.00 -	2,973.42	10.44	03/2015 03/2020	03/2020
	Total		16,643.70 -	26,719.91	4,305.32		
	ROAD TRANSPORT AND HIGHWAYS						
129	2-LANING WITH PS OF JHALAWAR-RAJASTHAN-MP. BORDER - [N24000237]	1/2014	177.32 -	177.32	86.65	01/2016 -	01/2016
130	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]	1/2014	270.00 -	270.00	-	03/2016 -	03/2016
131	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 -	208.00	290.60	04/2008 01/2017	01/2017
132	REHABILITATION & UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]	6/2014	260.39 -	260.39	-	11/2016 -	11/2016
133	NALBARI TO BIJNI (AS-6) - [N24000047]	12/2003	225.00 -	225.00	258.40	06/2008 04/2016	04/2016
134	REHABILITATION & UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN T - [N24000265]	11/2014	297.78 330.00	330.00	15.47	02/2017 -	02/2017
135	GUWAHATI TO NALBARI (AS-5) - [N24000046]	12/2003	198.16 -	198.16	-	04/2008 12/2015	12/2015

(November 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
136	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]	11/2013	1,916.79 -	1,916.79	-	11/2016 -	11/2016
137	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	30.08	12/2015 -	12/2015
138	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]	2/2015	241.61 -	241.61	23.83	02/2017 -	02/2017
139	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239]	1/2014	368.15 -	368.15	-	01/2016 -	01/2016
140	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	258.40	04/2010 02/2016	02/2016
141	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]	10/2014	244.30 -	244.30	-	12/2016 -	12/2016
142	GUWHATI TO NALBARI (AS-4) - [N24000038]	12/2003	175.96 -	175.96	182.50	04/2008 12/2015	12/2015
143	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236]	10/2013	677.79 -	677.79	59.09	04/2016 -	04/2016
144	REHABILITATION & UPGRADATION OF NH-222(61) FROM KM 161.570 TO 211.00 - [N24000255]	12/2013	220.72 -	220.72	-	11/2016 -	11/2016
145	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]	12/2013	177.18 -	177.18	-	03/2016 -	03/2016
146	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	1/2014	255.75 348.00	348.43	13.79	09/2017 -	09/2017
147	SONAPUR TO GUWAHTI (AS-3) - [N24000044]	12/2003	245.00 -	245.00	491.20	03/2008 04/2016	04/2016
148	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR - [N24000238]	1/2014	158.04 -	158.04	-	12/2015 -	12/2015
149	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]	3/2015	153.21 -	153.21	-	01/2017 -	01/2017
150	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTIO - [N24000242]	12/2013	158.65 -	158.65	-	03/2016 -	03/2016
151	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]	12/2003	160.00 -	160.00	197.60	05/2008 12/2015	12/2015
152	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]	1/2014	267.16 352.00	352.05	2.79	11/2017 -	11/2017
153	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]	3/2011	218.31 -	339.82	-	12/2015 -	12/2015
154	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]	10/2014	295.47 -	313.27	-	02/2017 -	02/2017

(November 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
155	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	4/2014	1,266.60 -	1,266.60	-	09/2016 -	09/2016
156	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]	6/2013	1,287.95 -	1,287.95	-	11/2015 -	11/2015
157	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]	1/2014	340.00 -	340.00	-	03/2016 -	03/2016
158	YAN TO NIRMAL SEREHALITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]	12/2013	244.08 -	244.08	-	03/2016 -	03/2016
159	CONSTRUCTION OF MAJOR/MINOR BRIDGE & ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOIA ROAD FROM KM 161 TO 45 - [N24000253]	8/2014	187.79 -	187.79	-	07/2016 -	07/2016
160	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]	3/2014	240.10 -	240.10	-	03/2016 -	03/2016
	Total		13,480.11 -	13,921.16	1,910.40		
	<u>STEEL</u>						
161	REBUILDING OF COB-7 AT BSL - [N12000083]	10/2013	245.67 -	245.67	68.15	05/2016 -	05/2016
162	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]	2/2014	4,749.00 -	4,749.00	1.29	09/2017 -	09/2017
163	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]	4/2015	3,127.30 -	3,127.30	156.76	04/2018 -	04/2018
164	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]	5/2015	1,154.18 -	1,154.18	17.72	12/2017 -	12/2017
165	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	33.61	10/2016 -	10/2016
166	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]	3/2015	1,034.01 -	1,034.01	-	10/2017 -	10/2017
167	ALTERNATE GAS NETWORK AT BSL - [N12000093]	3/2015	255.19 -	255.19	22.05	03/2018 -	03/2018
168	3RD CONVERTER AND 4TH CASTER - [N12000088]	7/2011	974.76 -	974.76	197.53	07/2016 -	07/2016
169	NMDC INTEGRATED STEEL PLANT - [N12000086]	1/2010	15,525.00 -	15,525.00	8,195.12	05/2015 12/2016	12/2016
170	TURBO BLOWER - 5 - [N12000092]	12/2009	280.00 -	280.00	15.77	09/2016 -	09/2016
	Total		27,688.11 -	27,833.51	8,708.00		
	<u>URBAN DEVELOPMENT</u>						
171	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]	2/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019

(November 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
172	NAGPUR METRO RAIL - [N28000085]	8/2014	8,680.00 -	8,680.00	-	03/2018 -	03/2018
173	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,219.21	-	07/2017 -	07/2017
174	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,264.00	759.17	11/2019 -	11/2019
175	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]	1/2009	225.81 -	225.81	136.53	06/2012 12/2015	12/2015
176	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]	4/2014	332.72 -	332.72	58.72	09/2016 01/2017	01/2017
177	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]	6/2014	157.84 -	157.84	-	03/2017 -	03/2017
178	KOCHI METRO RAIL PROJECT - [N28000081]	7/2012	5,181.79 -	5,181.79	-	07/2017 -	07/2017
	Total		46,466.51 -	46,466.51	954.42		
	Grand Total		356,290.74	381,848.71	91,487.98		

List of ongoing projects having cost overrun w.r.t. to revised schedule

(November 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00 -	09/2010 -	09/2016	62.57
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	22,462.00 -	12/2008 -	06/2016	70.54
	Total		16,663.00 -	28,139.00 -			
	<u>CIVIL AVIATION</u>						
3	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]	10/2012	217.60 -	244.10 -	03/2015 -	09/2015	12.18
	Total		217.60 -	244.10 -			
	<u>COAL</u>						
4	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59 -	03/2016 -	03/2016	31.87
5	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	479.63 -	03/2013 -	03/2017	0.02
	Total		630.12 -	678.22 -			
	<u>HEAVY INDUSTRY</u>						
6	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]	04/2011	1,718.00 -	3,827.30 -	09/2011 -	12/2017	122.78
	Total		1,718.00 -	3,827.30 -			
	<u>PETROCHEMICALS</u>						
7	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	9,965.00 -	04/2012 -	12/2015	82.49
	Total		5,460.61 -	9,965.00 -			
	<u>PETROLEUM</u>						
8	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	450.55 -	03/2017 -	03/2017	27.79
9	MARKETING TERMINAL AT PARADEEP - [N16000168]	07/2009	199.75 -	239.73 -	07/2013 -	11/2015	20.02

(November 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
10	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]	10/2013	429.06 -	429.06 -	10/2014 -	11/2015	0.00
11	MARKETING TOP AT KORBA - [N16000186]	01/2011	141.86 -	232.00 -	09/2016 -	03/2016	63.54
12	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	03/2012	14,225.00 -	16,504.00 -	05/2016 -	05/2016	16.02
13	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00 -	03/2015 -	08/2016	37.72
	Total		16,219.58 -	19,055.34 -			
	<u>POWER</u>						
14	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	7,818.68 -	09/2009 -	12/2018	99.48
15	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	18,063.89 -	09/2010 -	-	187.40
16	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]	09/2005	1,061.38 -	1,929.15 -	09/2009 -	06/2016	81.76
17	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203]	02/2015	302.49 302.00	302.49 -	02/2016 -	12/2015	0.00
18	BOKARO THERMAL POWER STATION-A - [N18000199]	08/2006	2,313.00 4,139.00	4,237.67 -	12/2011 -	03/2016	83.21
19	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]	04/2007	4,122.00 8,781.00	9,606.82 -	02/2011 -	01/2017	133.06
20	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,497.72 -	01/2016 -	11/2016	50.95
	Total		21,645.83 -	47,456.42 -			
	<u>RAILWAYS</u>						
21	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	36.80 274.41	1,336.57 -	- -	03/2019	3,531.98
22	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37 -	- -	02/2012	141.40
23	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 -	800.00 -	- -	-	414.30
24	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	492.98 -	1,727.27 -	12/2010 -	03/2018	250.37
25	GULBARGA-BIDAR,SCR(NL) - [220100254]	02/1998	242.42 369.70	844.00 -	- 05/2009	03/2015	248.16
26	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) [220100263]	03/1998	280.00 -	1,122.00 -	- -	-	300.71
27	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 -	1,047.00 -	- -	-	217.27

(November 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
28	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
29	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	02/2011 -	-	191.48
30	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	2,371.85	03/2005 12/2008	12/2019	2,019.62
31	JIND-SONEPAT (NL),NR - [220100280	01/2004	238.56 -	740.00	03/2012 -	12/2012	210.19
32	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06
33	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	03/2009 -	10/2015	156.57
34	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314	04/2001	470.92 727.13	1,225.90	- -	03/2017	160.32
35	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316	04/2003	218.19 -	343.00	- -	-	57.20
36	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	1,101.16	- -	03/2017	186.92
37	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	818.29	02/2015 -	-	346.59
38	CUTTACK - BARANG (LD) - [220100326	04/1995	127.13 -	225.00	- -	10/2014	76.98
39	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	276.00	03/2009 03/2009	-	106.88
40	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	810.78 -	810.80	- -	-	0.00
41	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329	04/2003	136.62 -	289.93	12/2007 03/2010	-	112.22
42	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045	03/1997	261.70 -	280.00	02/2006 -	-	6.99
43	BHOPAL BINA 3D LINE DOUBLING - [N22000077	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41
44	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079	09/2007	404.19 -	1,383.45	- -	-	242.28
45	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080	09/2006	343.17 -	914.98	- -	03/2016	166.63
46	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084	09/2006	125.00 -	490.00	- -	-	292.00
47	TIDIVANAM-NAGARI (NL) - [N22000085	09/2006	456.00 -	1,080.00	- -	-	136.84
48	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094	02/2008	171.10 -	275.08	03/2012 -	03/2016	60.77
49	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	619.34 -	2,820.25	04/2014 -	03/2018	355.36
50	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	332.92 283.95	477.88	03/2012 -	-	43.54

(November 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
51	VIRAMGAM-BHILDI(WR),GC - [N220100062	04/1990	155.66 -	548.01	- 03/2010	-	252.06
52	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032	04/2006	378.56 -	791.59	- -	-	109.11
53	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049	07/2006	743.00 -	1,117.11	03/2008 06/2008	-	50.35
54	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113	04/2008	653.19 -	653.55	03/2014 -	-	0.06
55	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120	04/2008	603.04 -	1,421.25	03/2012 -	-	135.68
56	KATAKHAL TO BHAIRABI - [N22000126	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41
57	WARDHA-NANDED MAHARASHTRA - [N22000231	04/2008	499.30 -	2,501.05	- -	-	400.91
58	KALYAN-KASARA 3RD LINE - [N22000233	04/2011	277.70 -	279.70	- -	-	0.72
59	PEN ROHA DOUBLING - [N22000254	04/2007	98.74 -	203.00	- -	03/2015	105.59
60	PANVEL PEN DOUBLING - [N22000255	04/2006	96.16 -	260.16	- -	01/2015	170.55
61	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256	04/2011	913.00 -	1,801.01	- -	-	97.26
62	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257	04/2007	179.65 -	1,350.91	- -	-	651.97
63	BAGALKOT-KUDACHI NL - [N22000258	04/2010	377.93 -	986.30	- -	-	160.97
64	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263	04/2008	184.26 -	2,000.00	- -	-	985.42
65	ROHTAK-MEHAM HANSI - [N22000272	04/2012	287.00 -	576.18	- -	-	100.76
66	BHANUPALI-BILASPUR BERI NL - [N22000273	04/2008	1,046.88 -	2,966.99	- -	-	183.41
67	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276	04/2013	558.00 -	692.43	- -	-	24.09
68	SRINIVASA-PURA-MADANAPALLI NL - [N22000277	04/2013	296.00 -	466.65	- -	-	57.65
69	SHIMOGA-HARIHAR NL - [N22000278	04/2011	562.74 -	832.47	- -	-	47.93
70	RAYADURGA-TUMKUR NL - [N22000279	04/2007	970.34 -	1,743.00	- -	-	79.63
71	WHITE FIELD-KOLAR NL - [N22000280	04/2011	341.05 -	348.85	- -	-	2.29
72	BHADRACHALAM ROAD-SATTUPALLI - [N22000287	04/2010	337.49 -	337.50	- -	-	0.00
73	HARIDWAR-LAKSAR - [N22000289	04/2012	219.83 -	329.97	- -	-	50.10
74	TORANAGALLU-RANJITPURA DL - [N22000298	04/2011	146.75 -	167.50	- -	-	14.14

(November 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
75	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00 -	- -	-	72.07
76	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77 -	- -	-	12.38
77	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]	04/1999	460.94 -	1,030.00 -	01/1999 -	-	123.46
78	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	800.00 -	01/1999 -	-	71.50
79	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00 -	01/1999 -	-	53.96
80	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	514.68 -	2,820.00 -	- -	-	447.91
81	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	1,781.98 -	03/2004 -	03/2016	259.68
82	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	09/1997	1,500.00 -	4,996.19 -	04/2008 12/2011	06/2017	233.08
83	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	1,630.97 -	05/2008 -	-	558.55
84	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	04/1997	501.69 335.77	1,043.56 -	03/2012 -	-	108.01
85	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72 -	12/2009 -	06/2015	300.67
86	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	541.00 -	- -	-	232.17
87	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	2,531.34 -	12/2008 -	03/2018	245.34
88	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	470.21 -	1,995.25 -	- -	-	324.33
89	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	6,570.75 -	03/2011 -	03/2019	803.12
90	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	322.95 -	341.41 -	03/2012 -	-	5.72
91	PATNA GANGA BRIDGE (NL), ECR - [220100308]	04/2001	624.47 -	2,921.00 -	10/2007 -	12/2015	367.76
92	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	485.00 -	03/2011 -	-	185.29
93	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	496.24 -	- -	03/2017	148.12
94	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	300.00 -	827.73 -	- -	03/2019	175.91
95	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	850.00 -	2,973.42 -	03/2015 -	03/2020	249.81
96	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04 -	03/2014 -	03/2019	50.68

(November 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
97	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	5,500.00	03/2009 -	03/2016	228.10
98	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	2,876.00	03/2014 -	03/2018	253.60
99	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	565.13	-	03/2018	99.75
100	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,190.00	12/2015 -	03/2020	212.81
101	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]	03/1997	677.97 1,062.36	1,651.54	-	03/2018	143.60
102	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
103	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60
104	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	625.30 408.76	847.75	06/2007 -	-	35.57
105	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,564.54	03/2010 -	03/2017	381.40
106	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]	04/1995	304.00 -	968.60	12/2012 -	-	218.62
107	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 -	288.00	02/2009 02/2009	-	73.33
108	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	385.54	03/2010 -	-	18.66
109	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	155.74 164.36	883.00	02/2009 -	03/2015	466.97
110	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	218.24 236.41	645.00	-	03/2015	195.55
111	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
112	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30 -	1,544.40	03/1998 -	12/2019	299.79
113	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	03/2015	160.76
114	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,428.00	06/2005 -	12/2019	385.76
115	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	194.07 -	335.00	06/2004 -	12/2015	72.62
116	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	227.00 -	2,135.00	-	-	840.53
117	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]	02/1997	295.00 -	1,289.92	-	-	337.26
118	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	04/1996	138.00 -	1,382.78	-	-	902.01
119	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]	04/2007	482.00 -	874.57	03/2013 -	09/2015	81.45

(November 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
120	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [N220100262	09/1995	100.00 -	980.00	- -	-	880.00
121	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123	04/2008	318.24 -	321.62	03/2012 -	-	1.06
122	SAMBALPUR-TALCHER DOUBLING - [N22000315	03/2011	679.27 -	1,111.99	- -	-	63.70
123	JHARSUGUDA-RENGALI DOUBLING - [N22000317	03/2006	201.00 -	230.00	- -	-	14.43
124	KIRANDUL - JAGDALPUR DOUBLING - [N22000318	12/2012	826.57 -	1,143.60	- -	03/2018	38.35
125	DELANG-PURI DOUBLING - [N22000320	03/2011	165.16 -	234.71	03/2015 -	-	42.11
126	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321	04/2014	182.92 -	197.73	- -	-	8.10
127	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	04/2012	148.77 -	209.00	12/2016 -	12/2016	40.49
128	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [N220100106	12/1994	124.43 -	925.30	- -	02/2014	643.63
129	AMRAVATI-NARKHER NL(CR) - [N220100118	06/1994	663.01 175.30	725.00	06/1999 -	07/2012	9.35
130	ANGAMALI-SABARIMALA (N.L.)(SR) - [N220100252	10/1998	550.00 -	1,566.00	- -	-	184.73
131	CHHAPRA-BALLIA UP - [N22000134	03/2013	295.00 -	494.92	- -	-	67.77
132	VIRAMGAM-SAMAKHIALI (DL) - [N22000145	04/2011	446.00 -	685.17	- -	-	53.63
133	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147	04/2011	2,082.75 -	3,500.00	- -	-	68.05
134	THIYAT HAMIRA-SANU - [N22000149	04/2013	236.93 -	262.00	- -	-	10.58
135	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTISURGARH-UDAIPUR [N22000152	04/2013	456.00 -	855.16	- -	-	87.54
136	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153	04/2010	739.65 -	872.22	- -	-	17.92
137	AJMER-BANGURGRAM - [N22000155	04/2011	213.39 -	218.39	- -	-	2.34
138	BOWAICHANDI-ARAMBAGH - [N22000159	04/2010	267.37 -	434.00	- -	-	62.32
139	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160	04/2010	553.63 -	1,009.00	- -	12/2019	82.25
140	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161	04/2011	289.64 -	760.00	- -	-	162.39
141	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44
142	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164	04/2010	309.44 -	583.00	12/2015 -	03/2016	88.40

(November 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
143	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	12/2017	41.36
144	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
145	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
146	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	- -	-	338.91
147	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
148	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00 -	1,887.90	- -	03/2019	5.00
149	ATTIPPATTU-PUTTUR - [N22000184]	04/2008	446.87 -	528.00	- -	-	18.16
150	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,200.00	- -	-	129.22
151	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
152	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17
153	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC [N22000188]	04/1998	271.24 -	520.00	- -	-	91.71
154	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,280.83	- -	-	55.74
155	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
156	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	563.13	- -	03/2019	154.33
157	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,242.25	03/2007 -	03/2016	38.80
158	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00 -	886.65	- -	03/2018	251.85
159	DIMAPUR-TIZIT NL - [N22000196]	04/2013	4,274.00 -	4,487.70	- -	03/2020	5.00
160	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77 -	441.45	- -	03/2018	110.44
161	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	288.81	- -	03/2018	1.86
162	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22	- -	-	109.04
163	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	-	173.71
164	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	247.00 -	951.24	- -	03/2015	285.12
165	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	222.95	- -	-	16.29

(November 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
166	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02 -	5,307.90	- -	03/2020	30.00
167	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	679.57	- -	03/2018	180.56
168	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	03/2017	63.25
169	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	435.58	- -	03/2018	162.68
170	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]	04/1999	523.17 -	1,653.55	- -	03/2018	216.06
171	AMBAR FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12 -	453.10	- -	03/2018	45.17
172	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	364.06	- -	03/2019	47.95
173	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	03/2016	29.06
174	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	800.00	- -	-	33.02
	Total		79,170.45 -	200,328.20			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
175	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	-	28.93
176	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	-	92.75
177	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	-	80.68
178	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	-	68.99
179	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	-	106.50
180	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00 -	201.66	09/2008 -	-	30.10
181	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	-	2.29
182	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]	10/2014	295.47 -	313.27	02/2017 -	02/2017	6.02
183	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH- 202 UNDER LWE S - [N24000249]	03/2011	218.31 -	339.82	12/2015 -	12/2015	55.66
184	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	01/2014	255.75 348.00	348.43	09/2017 -	09/2017	36.24

(November 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
185	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	01/2014	267.16 352.00	352.05	11/2017 -	11/2017	31.78
186	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262	12/2014	201.12 201.00	201.12	02/2015 -	-	0.00
	Total		3,606.66 -	5,683.15			
	<u>SHIPPING AND PORTS</u>						
187	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016	11/2007	1,228.00 -	1,460.00	12/2010 -	09/2017	18.89
188	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	12/2015	300.00
189	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059	03/2007	245.67 -	409.83	04/2009 -	08/2016	66.82
	Total		1,623.67 -	2,469.83			
	<u>STEEL</u>						
190	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	10/2016	42.39
	Total		343.00 -	488.40			
	<u>URBAN DEVELOPMENT</u>						
191	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00 -	11,609.00	06/2011 -	-	81.53
	Total		6,395.00 -	11,609.00			
	Grand Total		153,693.52	329,943.96			

List of Delayed Projects w.r.t. Latest Schedule

(November 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL, TAMIL NADU	12/2001	13,171.00 17,270.00	22,462.00	20,962.00	12/2008 10/2013	06/2016	90	32
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVINI, TAMIL NADU	09/2003	3,492.00 -	5,677.00	-	09/2010 -	09/2016	72	-
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 -	11,459.00	7,477.00	12/2015 10/2016	10/2017	22	12
4	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 -	12,320.00	5,279.00	12/2016 04/2017	05/2018	17	13
	Total		40,442.00 -	51,918.00	33,718.00				
	<u>CIVIL AVIATION</u>								
5	CONSTRUCTION OF NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT - [N04000050]AAI, SIKKIM	01/2009	309.46 -	309.46	404.81	01/2011 06/2016	09/2017	80	15
	Total		309.46 -	309.46	404.81				
	<u>COAL</u>								
6	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL, ODISHA	01/2005	302.96 -	302.96	297.02	03/2010 -	03/2016	72	-
7	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL, CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,920.50	03/2014 -	03/2016	24	-
8	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL, CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,701.89	03/2014 -	03/2016	24	-
9	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL, UTTAR PRADESH	06/2011	789.88 741.62	741.62	493.43	03/2013 -	03/2016	36	-
10	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL, MADHYA PRADESH	06/2011	746.04 535.10	535.10	412.91	03/2015 -	03/2016	12	-
11	ADRIYALA SHAFT PROJECT - [N06000016]SCCL, TELANGANA	12/2009	212.34 1,228.39	1,228.39	861.82	03/2013 09/2012	03/2016	36	42
12	CHURCHA ROUG (1.35 MTY) - [N06000046]SECL, CHHATISGARH	06/2008	462.35 -	462.35	298.87	03/2014 -	03/2016	24	-
13	RAJMAHAL OC EXP. - [N06000056]ECL, JHARKHAND	09/2009	153.82 -	153.82	67.34	03/2014 -	03/2016	24	-
14	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL, TELANGANA	12/2009	418.97 -	418.97	365.11	03/2012 -	03/2016	48	-
15	RKP OCP PHASE-I - [N06000079]SCCL, TELANGANA	03/2010	209.78 -	209.78	73.19	03/2015 -	03/2016	12	-
16	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL, TELANGANA	03/2010	181.19 -	181.19	64.25	03/2012 -	03/2016	48	-
17	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL, JHARKHAND	08/2007	163.51 -	163.51	35.96	03/2011 -	03/2016	60	-
18	PURNADIH OCP (3.0 MTY) - [N06000085]CCL, JHARKHAND	07/2008	210.98 -	210.98	-	03/2013 -	03/2016	36	-

(November 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
19	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68	264.68	-	03/2012	03/2016	48	-
20	MURADIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88	339.88	12.06	04/2014	03/2016	23	-
21	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]NLC,TAMIL NADU	04/2012	364.75	364.75	182.79	10/2014	03/2016	17	-
22	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45	289.45	98.72	05/2014	10/2016	29	-
23	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82	269.82	55.36	04/2014	11/2016	31	-
24	ASHOK EXPN OCP CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	341.63	341.63	126.41	03/2011	03/2017	72	-
25	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL	11/2006	287.18	287.18	226.26	03/2011	03/2017	72	-
26	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77	457.77	206.83	03/2013	03/2017	48	-
27	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08	172.08	150.27	03/2010	03/2017	84	-
28	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63	453.63	101.64	12/2012	03/2017	51	-
29	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28	207.28	205.79	03/2012	03/2017	60	-
30	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53	479.63	175.64	03/2013	03/2017	48	-
31	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87	179.87	-	03/2012	03/2017	60	-
32	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46	162.46	70.05	03/2014	03/2017	36	-
33	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01	365.01	6.56	06/2015	03/2017	21	-
34	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33	417.33	14.13	07/2016	03/2017	8	-
35	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03	249.03	76.65	03/2012	03/2018	72	-
36	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50	321.50	209.59	03/2014	03/2018	48	-
37	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29	242.29	0.03	03/2015	03/2018	36	-
38	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06	447.06	29.03	03/2015	03/2018	36	-
39	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56	258.56	96.39	03/2016	03/2018	24	-
40	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76	162.76	1.31	03/2015	03/2019	48	-
41	TALABIRA OCP - [N06000043]MCL,ODISHA	03/2008	447.72	447.72	52.36	03/2016	03/2020	48	-
42	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH	09/2008	152.43	152.43	24.72	03/2015	03/2020	60	-
43	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44	178.44	0.30	03/2014	03/2020	72	-
44	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	706.40	706.40	77.72	07/2012	03/2021	104	-

(November 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
45	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL, ODISHA	02/2008	395.87 -	395.87	-	03/2015 -	03/2021	72	-
	Total		17,085.56 -	17,842.51	8,792.90				
	<u>STEEL</u>								
46	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]SAIL, WEST BENGAL	11/2012	313.05 -	313.05	301.82	06/2015 -	12/2015	6	-
47	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL, ODISHA	10/2012	160.48 -	160.48	142.58	09/2014 -	12/2015	15	-
48	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH - [N12000078]SAIL, CHHATISGARH	07/2012	332.65 -	332.65	222.78	08/2014 -	01/2016	17	-
49	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODISHA - [N12000079]SAIL, ODISHA	06/2012	237.09 -	237.09	216.21	12/2014 -	01/2016	13	-
50	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL, MAHARASHTRA	12/2011	187.33 -	187.33	171.52	10/2013 -	03/2016	29	-
51	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, CHHATISGARH	08/2010	17,265.00 -	17,265.00	15,279.06	03/2013 -	06/2016	39	-
52	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL, ANDHRA PRADESH	07/2011	877.73 -	877.73	332.82	07/2015 -	06/2016	11	-
53	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]SAIL, ODISHA	06/2014	708.91 -	708.91	245.17	04/2016 -	08/2016	4	-
54	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL, ANDHRA PRADESH	05/2012	404.16 -	404.16	248.15	07/2015 -	03/2017	20	-
	Total		20,486.40 -	20,486.40	17,160.11				
	<u>PETROCHEMICALS</u>								
55	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, ASSAM	04/2006	5,460.61 8,920.00	9,965.00	9,025.14	04/2012 12/2013	12/2015	44	24
	Total		5,460.61 -	9,965.00	9,025.14				
	<u>PETROLEUM</u>								
56	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL, MAHARASHTRA	03/2012	1,419.00 -	1,419.00	1,284.80	12/2014 -	11/2015	11	-
57	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]ONGC, MULTI STATE	10/2013	429.06 429.00	429.06	439.02	10/2014 10/2015	11/2015	13	1
58	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL, MULTI STATE	08/2011	586.00 -	586.00	400.66	08/2015 -	12/2015	4	-
59	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL, TAMIL NADU	12/2012	279.00 -	279.00	186.74	12/2014 -	12/2015	12	-
60	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL, JHARKHAND	04/2011	191.96 -	191.96	96.98	05/2015 -	12/2015	7	-
61	PARADIP REFINERY PROJECT - [N16000058]IOCL, ODISHA	02/2009	29,777.00 34,555.00	34,555.00	30,413.42	11/2012 11/2013	01/2016	38	26

(November 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
62	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	251.66	-	06/2012 11/2015	01/2016	43	2
63	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	1,250.50	09/2012 -	03/2016	42	-
64	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA	12/2009	1,584.00 -	1,584.00	1,353.89	08/2015 -	03/2016	7	-
65	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	463.32	314.41	06/2011 03/2012	03/2016	57	48
66	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	317.64 -	240.95	123.32	09/2012 12/2015	03/2016	42	3
67	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]SPRL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	1,016.37	10/2011 -	03/2016	53	-
68	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]SPRL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,438.30	01/2012 -	03/2016	50	-
69	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL,GUJARAT	12/2011	160.00 -	160.00	31.28	02/2016 02/2016	03/2016	1	1
70	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 1,256.72	1,256.72	989.16	05/2013 12/2015	04/2016	35	4
71	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17 600.17	600.17	375.14	12/2014 05/2015	05/2016	17	12
72	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 686.58	686.58	540.72	04/2015 04/2015	05/2016	13	13
73	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	736.65	498.95	09/2011 12/2015	06/2016	57	6
74	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]IOCL,BIHAR	04/2013	480.00 -	480.00	85.08	02/2016 -	07/2016	5	-
75	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	1,200.00	432.84	03/2015 11/2015	08/2016	17	9
76	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	913.00	455.18	08/2015 -	12/2016	16	-
77	CRU TO ISOMERIZATION (ISOM) - [N16000200]BPCL,MULTI STATE	10/2011	725.00 -	725.00	80.59	11/2016 -	12/2016	1	-
78	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 2,378.89	2,378.89	1,789.38	03/2013 03/2016	03/2017	48	12
79	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL, WEST BENGAL	03/2014	3,076.00 -	3,076.00	112.15	09/2017 -	12/2017	3	-
80	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	3,957.00 3,561.00	3,561.00	24.73	01/2013 -	12/2018	71	-
	Total		54,819.59 -	60,486.96	43,733.61				
	POWER								

(November 2015)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
81	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	342.05	02/2012 -	12/2015	46	-
82	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	546.58	02/2014 -	12/2015	22	-
83	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	753.44	11/2012 -	01/2016	38	-
84	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 2,348.37	2,348.37	1,914.09	03/2013 06/2015	01/2016	34	7
85	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,436.11	04/2013 -	01/2016	33	-
86	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	184.17	01/2013 -	01/2016	36	-
87	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL,MULTI STATE	02/2012	1,927.16 -	1,927.16	1,564.24	10/2014 -	01/2016	15	-
88	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	269.39	05/2015 -	01/2016	8	-
89	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	489.81	11/2013 -	02/2016	27	-
90	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	2,301.62	08/2014 -	02/2016	18	-
91	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 346.79	346.79	289.16	08/2014 06/2015	02/2016	18	8
92	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,060.56	08/2012 -	03/2016	43	-
93	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,536.72	11/2013 -	03/2016	28	-
94	KBUNL-MUZAFFARPUR TPP STAGE-II-SUBSIDIARY (2X195 MW) - [N18000191]JNTPC,BIHAR	03/2010	3,984.03 -	3,984.03	3,096.26	01/2013 -	03/2016	38	-
95	BOKARO THERMAL POWER STATION-A - [N18000199]DVC,JHARKHAND	08/2006	2,313.00 4,139.00	4,237.67	3,088.00	12/2011 -	03/2016	51	-
96	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]NHPC,WEST BENGAL	09/2005	1,061.38 -	1,929.15	1,923.42	09/2009 -	06/2016	81	-
97	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 721.81	721.81	555.26	09/2010 06/2013	06/2016	69	36
98	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	500.24	11/2011 -	06/2016	55	-
99	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	2,219.30	12/2012 -	06/2016	42	-

(November 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
100	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 689.03	689.03	515.20	07/2013 11/2015	06/2016	35	7
101	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATISGARH	05/2011	1,961.87 -	1,961.87	1,757.69	05/2014 -	06/2016	25	-
102	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,864.76	09/2014 -	06/2016	21	-
103	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH	11/2011	2,127.51 -	2,127.51	2,287.68	07/2014 -	06/2016	23	-
104	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 2,228.71	2,228.71	1,475.50	08/2014 12/2015	06/2016	22	6
105	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATISGARH	01/2012	1,422.85 -	1,422.85	1,349.97	01/2015 -	06/2016	17	-
106	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	90.74	09/2014 -	06/2016	21	-
107	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATISGARH	03/2012	9,569.76 -	9,569.76	5,312.24	06/2015 -	06/2016	12	-
108	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	554.56	11/2014 -	06/2016	19	-
109	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	2,869.07	10/2014 -	06/2016	20	-
110	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 -	196.58	5.10	02/2016 -	06/2016	4	-
111	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	277.30	06/2015 -	08/2016	14	-
112	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	956.42	06/2015 -	08/2016	14	-
113	KISHANGANGA HEP (3X110 MW) - [N18000031]JNHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,497.72	4,276.75	01/2016 -	11/2016	10	-
114	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	5.36	04/2016 -	11/2016	7	-
115	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	4,181.23	10/2012 -	12/2016	50	-
116	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 -	4,404.57	2,357.96	01/2015 -	12/2016	23	-

(November 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
117	EASTERN REGION STRENGTHENING SCHEME- III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80	1,272.80	1,219.55	11/2012	12/2016	49	-
118	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88	2,514.88	1,043.56	12/2015	12/2016	12	-
119	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]DVC,WEST BENGAL	04/2007	4,122.00	9,606.82	1,353.36	02/2011	01/2017	71	-
120	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35	6,749.18	5,588.00	09/2011	03/2017	66	-
121	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	01/2012	15,166.19	15,166.19	9,676.00	01/2017	03/2017	2	-
122	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18	9,395.18	5,620.00	11/2016	08/2017	9	-
123	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42	195.42	40.43	02/2014	09/2017	43	-
124	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00	5,353.00	5,129.27	05/2014	09/2017	40	-
125	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89	9,750.89	4,233.50	12/2016	09/2017	9	-
126	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97	15,095.67	11,012.00	01/2011	05/2018	88	43
127	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59	7,818.68	5,328.26	09/2009	12/2018	111	-
128	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48	3,846.30	2,631.00	03/2013	12/2018	69	-
129	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00	2,978.86	1,498.91	02/2016	09/2019	43	43
130	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58	2,491.58	752.82	06/2013	12/2019	78	-
131	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29	2,159.07	1,897.65	11/2008	12/2016	97	57
	Total		138,127.40	164,490.96	111,232.26				
	HEAVY INDUSTRY								
132	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]HIPE,MULTI STATE	04/2011	1,718.00	3,827.30	-	09/2011	12/2017	75	-
	Total		1,718.00	3,827.30	.00				
	HEALTH AND FAMILY WELFARE								
133	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57	175.57	89.92	12/2014	03/2016	15	-
	Total		175.57	175.57	89.92				
	RAILWAYS								
134	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07	335.00	230.67	06/2004	12/2015	138	-

(November 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
135	PATNA GANGA BRIDGE (NL), ECR - [220100308]JECR,BIHAR	04/2001	624.47 -	2,921.00	2,521.72	10/2007 12/2012	12/2015	98	36
136	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	800.00	793.71	03/2010 -	12/2015	69	-
137	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 495.44	1,781.98	440.08	03/2004 -	03/2016	144	-
138	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	275.08	141.55	03/2012 12/2013	03/2016	48	27
139	KATAKHAL TO BHAIKABI - [N22000126]NFR,ASSAM	04/1998	227.90 200.00	331.40	182.22	12/2012 -	03/2016	39	-
140	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 -	5,500.00	4,734.45	03/2009 -	03/2016	84	-
141	DANGOAPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	583.00	144.66	12/2015 -	03/2016	3	-
142	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 575.00	1,242.25	1,005.81	03/2007 -	03/2016	108	-
143	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	204.56	03/2016 -	06/2016	3	-
144	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	230.00	68.67	03/2015 -	12/2016	21	-
145	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	714.10	65.93	04/2016 -	03/2017	11	-
146	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 1,000.00	4,996.19	3,410.06	04/2008 03/2014	06/2017	110	39
147	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	1,727.27	743.74	12/2010 -	03/2018	87	-
148	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	733.00 733.00	2,531.34	1,732.43	12/2008 -	03/2018	111	-
149	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 813.34	2,876.00	823.83	03/2014 -	03/2018	48	-
150	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34 619.34	2,820.25	199.31	04/2014 03/2015	03/2018	47	36
151	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	4,874.58	1,911.65	03/2016 -	06/2018	27	-
152	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	19,565.00	10,658.34	11/2002 -	12/2018	193	-
153	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 727.56	6,570.75	2,787.99	03/2011 03/2014	03/2019	96	60
154	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,157.54	1,544.40	590.26	03/1998 -	12/2019	261	-
155	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	2,371.85	486.25	03/2005 12/2008	12/2019	177	132
156	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97 1,013.74	1,428.00	466.36	06/2005 07/2011	12/2019	174	101
157	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 1,339.48	4,190.00	88.56	12/2015 -	03/2020	51	-

(November 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	Total		22,935.10	72,607.16	34,432.81				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
158	REHABILITATION & UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE-DORNALA T-JUNCTION) T - [N24000267]PWD, ANDHRA PRADESH	02/2014	258.99	258.99	64.65	07/2014	07/2016	24	-
159	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD, ANDHRA PRADESH	07/2014	251.55	251.55	-	02/2015	02/2017	24	-
	Total		510.54	510.54	64.65				
	<u>SHIPPING AND PORTS</u>								
160	ENMORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST, TAMIL NADU	10/2002	150.00	600.00	139.80	03/2006	12/2015	117	-
161	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU, MAHARASHTRA	01/2007	366.39	669.46	412.00	12/2010	01/2016	61	-
162	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL, KERALA	03/2007	245.67	409.83	353.18	04/2009	08/2016	88	77
163	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016]MUMBAI PORT TRU, MAHARASHTRA	11/2007	1,228.00	1,460.00	1,038.00	12/2010	09/2017	81	-
	Total		1,990.06	3,139.29	1,942.98				
	<u>TELECOMMUNICATIONS</u>								
164	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL, MULTI STATE	10/2009	384.00	384.00	74.74	10/2010	11/2015	61	3
	Total		384.00	384.00	74.74				
	<u>URBAN DEVELOPMENT</u>								
165	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL, MAHARASHTRA	07/2013	23,136.00	23,136.00	-	01/2015	12/2015	11	-
166	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD, DELHI	07/2012	884.30	884.30	-	08/2014	01/2016	17	-
167	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD, HIMACHAL PRADESH	11/2012	270.83	270.83	57.69	11/2014	03/2016	16	-
168	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD, DELHI	05/2012	405.01	405.01	-	12/2014	04/2016	16	-

(November 2015)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
169	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 171.86	171.86	8.64	03/2016 -	05/2016	2	-
170	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85 -	261.85	150.77	05/2013 10/2015	06/2016	37	8
171	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 14,600.00	14,600.00	11,544.24	12/2015 -	08/2016	8	-
172	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	38,585.00	18,738.92	03/2016 -	12/2016	9	-
173	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	188.87	5.79	12/2014 -	12/2016	24	-
174	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	18.65	09/2015 07/2016	12/2016	15	5
	Total		78,660.29 -	78,660.29	30,524.70				
	Grand Total		383,104.58	484,803.44	291,196.63				

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	05/2018	12320	17
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	10/2017	11459	22
3	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	06/2016	13171	90
4	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	09/2016	3492	72

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
5	CONSTRUCTION OF NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT	AAI	01/2009	01/2011	09/2017	309.46	80

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
6	KALYANIKHANI OPENCAST PROJECT	SCCL	07/2012	07/2016	03/2017	417.33	8
7	RG OC -III EXTENSION (PHASE -II) PROJECT	SCCL	06/2012	06/2015	03/2017	365.01	21
8	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2019	162.76	48
9	BAROUD OC EXPANSION (RCE)- 3MTY	SECL	04/2012	03/2016	03/2018	258.56	24
10	BLOCK-B OCP NCL (3.5 MTY)	NCL	06/2011	03/2015	03/2016	746.04	12
11	MOONIDIH XV SEAM UG	BCCL	08/2011	04/2015	04/2019	1230.27	48
12	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2009	03/2014	03/2018	321.5	48
13	GOPAL PRASAD OCP (15MTY)	MCL	02/2008	03/2015	03/2021	395.87	72
14	TALABIRA OCP	MCL	03/2008	03/2016	03/2020	447.72	48
15	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	03/2012	03/2017	207.28	60
16	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2017	479.53	48
17	RKP OCP PHASE-I	SCCL	03/2010	03/2015	03/2016	209.78	12
18	BALRAM OCP EXTENSION, MCL 8.00 MTY	MCL	12/2007	03/2010	03/2017	172.08	84
19	GEVRA EXPANSION OCP (SECL) (25-35) MTY	SECL	06/2010	03/2014	03/2016	2675.67	24
20	DIPKA EXPANSION OCP (SECL) (20-25) MTY	SECL	12/2009	03/2014	03/2016	1943.66	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
21	TAPIN OCP (2.5 MTY)	CCL	08/2008	03/2012	03/2016	264.68	48
22	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2017	162.46	36
23	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2018	249.03	72
24	JHANJRA R-VI SEAM PSLW	ECL	11/2006	03/2011	03/2017	287.18	72
25	RAJMAHAL OC EXP.	ECL	09/2009	03/2014	03/2016	153.82	24
26	KAKATIYA LONGWALL	SCCL	12/2008	12/2012	03/2017	453.63	51
27	KISTARAM OCP	SCCL	11/2010	03/2015	03/2018	242.29	36
28	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2020	178.44	72
29	MANUGURU OC-II EXTENSION PHASE-II	SCCL	03/2010	03/2012	03/2016	181.19	48
30	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	60
31	MAGADH OC 20 MTY (CCL)	CCL	08/2008	07/2012	03/2021	706.4	104
32	KRISHNASHILA (NCL) (4MTY)	NCL	06/2011	03/2013	03/2016	789.88	36
33	ASHOK EXPN OCP CCL (10 MTY)	CCL	12/2007	03/2011	03/2017	341.63	72
34	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	03/2017	259.4	60
35	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2016	418.97	48
36	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2016	163.51	60
37	PURNADIH OCP (3.0 MTY)	CCL	07/2008	03/2013	03/2016	210.98	36
38	NORTH URIMARI OCP (3.0 MTY)	CCL	12/2007	03/2012	03/2017	179.87	60
39	WIND POWER PROJECT, KAZHUNEERKULAM, TAMILNADU	NLC	04/2012	10/2014	03/2016	364.75	17
40	ADRIYALA SHAFT PROJECT	SCCL	12/2009	03/2013	03/2016	212.34	36
41	MADHUBAND NLW WASHERY	BCCL	08/2010	05/2014	10/2016	289.45	29
42	PATHERDIH NLW WASHERY	BCCL	10/2012	04/2014	11/2016	269.82	31
43	KULDA OCP (MAHANADI COALFIELDS LTD)	MCL	01/2005	03/2010	03/2016	302.96	72

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
44	CHURCHA ROUG (1.35MTY)	SECL	06/2008	03/2014	03/2016	462.35	24
45	KANIHA OCP, MCL, (10.0 MTY)	MCL	12/2007	03/2013	03/2017	457.77	48
46	MURAIIDH UG TURN-KEY PROJECT	BCCL	02/2011	04/2014	03/2016	339.88	23
47	JALAGAM VENGALA RAO OCP-II	SCCL	07/2011	03/2015	03/2018	447.06	36
48	NEYVELI NEW THERMAL POWER PROJECT (2X500 MW)	NLC	06/2011	12/2015	04/2018	5907.11	28

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
49	LGBRIMH-TEZPUR, ASSAM	HSCC	07/2012	12/2014	03/2016	175.57	15

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
50	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	HIPE	04/2011	09/2011	12/2017	1718	75

PETROCHEMICALS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
51	ASSAM GAS CRACKER PROJECT	BCPL	04/2006	04/2012	12/2015	5460.61	44

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
52	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	08/2016	871.35	17
53	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	ISPRL	01/2006	10/2011	03/2016	732	53
54	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	11/2016	666	12
55	IOR OF B-173A FIELD	ONGC	01/2012	03/2014	05/2016	352.49	26
56	INTEGRATED DEVELOPMENT OF BASSEIN FIELD	ONGC	12/2012	02/2016	12/2017	3513.07	22
57	RECONSTRUCTION OF BPA AND BPB PLATFORMS	ONGC	03/2013	04/2015	05/2016	1138.5	13
58	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS (OSV)	ONGC	06/2007	09/2011	06/2016	736.65	57
59	DEVELOPMENT OF WO-16 CLUSTER FIELDS	ONGC	06/2010	01/2014	12/2015	2523	23

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
60	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG	OIL	04/2010	06/2012	01/2016	270	43
61	MARKETING TERMINAL AT PARADEEP	IOCL	07/2009	07/2013	11/2015	199.75	28
62	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	03/2016	993	50
63	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	12/2017	4124.35	20
64	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE	ONGC	04/2013	04/2015	05/2017	284.82	25
65	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1)	ONGC	10/2013	10/2014	11/2015	429.06	13
66	RESID UPGRADATION PROJECT	CPCL	02/2011	11/2015	07/2016	3110.36	8
67	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND)	IOCL	04/2011	05/2015	12/2015	191.96	7
68	DAMAN DEVELOPMENT PROJECT	ONGC	08/2014	05/2019	03/2020	6086.08	10
69	CONSTRUCTION OF 6 ETPS	ONGC	03/2009	09/2012	03/2016	317.64	42
70	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I	GAIL	07/2009	01/2013	12/2018	3957	71
71	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT (MOPS)	ONGC	03/2011	05/2013	04/2016	861.79	35
72	PARADIP-RAIPUR- RANCHI PIPELINE	IOCL	08/2009	09/2012	03/2016	1793	42
73	DE-BOTTLENECKING OF SMPL	IOCL	12/2009	08/2015	03/2016	1584	7
74	PARADIP REFINERY PROJECT	IOCL	02/2009	11/2012	01/2016	29777	38
75	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH)	GAIL	12/2009	06/2011	03/2016	463.32	57
76	ASSAM RENEWAL PROJECT FOR GROUP A	ONGC	03/2009	03/2013	03/2017	2465.15	48
77	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	05/2016	2059.63	14
78	DEVELOPMENT OF C-26 CLUSTER FIELDS	ONGC	03/2012	05/2014	05/2016	2592.17	24
79	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD	ONGC	04/2012	12/2014	05/2016	600.17	17
80	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY	BPCL	03/2012	12/2014	11/2015	1419	11
81	PARADIP HALDIA DURGAPUR LPG PIPELINE	IOCL	02/2011	08/2015	12/2016	913	16
82	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	03/2017	309.81	29

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
83	MOUNDED BULLET PROJECT AT CPCL	CPCL	12/2012	12/2014	12/2015	279	12

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
84	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI	PGCIL	06/2012	06/2015	08/2016	1909.24	14
85	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A	PGCIL	09/2010	03/2013	01/2016	2074.86	34
86	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH	PGCIL	05/2011	05/2014	06/2016	1961.87	25
87	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2018	2978.48	69
88	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	03/2017	4375.35	66
89	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI	PGCIL	07/2010	07/2013	06/2016	752.64	35
90	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A	PGCIL	05/2010	01/2013	01/2016	250.03	36
91	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	12/2016	1272.8	49
92	DHUKWAN SMALL HYDRO PROJECT	THDCIL	05/2011	02/2014	09/2017	195.42	43
93	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	09/2017	5353	40
94	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2018	3919.59	111
95	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	NHPC	09/2005	09/2009	06/2016	1061.38	81
96	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	06/2016	477.69	69
97	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX	PGCIL	02/2009	02/2012	12/2015	410.29	46
98	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	12/2016	4824.12	50
99	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI	PGCIL	08/2010	04/2013	01/2016	1677.57	33
100	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME	PGCIL	03/2010	11/2012	01/2016	965.58	38
101	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B	PGCIL	03/2011	11/2013	03/2016	1585.12	28
102	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII	PGCIL	02/2009	11/2011	06/2016	509.66	55
103	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER	PGCIL	04/2010	01/2015	12/2016	4404.57	23

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
104	KBUNL-MUZAFFARPUR TPP STAGE-II-SUBSIDIARY (2X195 MW)	NTPC	03/2010	01/2013	03/2016	3984.03	38
105	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	12/2016	09/2017	9750.89	9
106	BOKARO THERMAL POWER STATION-A	DVC	08/2006	12/2011	03/2016	2313	51
107	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	DVC	04/2007	02/2011	01/2017	4122	71
108	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2019	2491.58	78
109	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2	PGCIL	12/2011	08/2014	02/2016	2422.66	18
110	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	12/2016	2496.9	84
111	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	12/2011	08/2014	06/2016	1746.65	22
112	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	12/2017	11130.19	52
113	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP)	PGCIL	12/2009	08/2012	03/2016	1216.83	43
114	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	06/2016	2144	42
115	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	PGCIL	01/2014	04/2016	11/2016	374.63	7
116	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	11/2016	3642.04	10
117	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	12/2016	1779.29	97
118	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	05/2018	8692.97	88
119	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	01/2012	01/2015	06/2016	1422.85	17
120	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	10/2017	368.72	135
121	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	12/2015	421.01	29
122	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B	PGCIL	02/2012	10/2014	01/2016	1927.16	15
123	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION	PGCIL	03/2012	09/2014	06/2016	198.63	21
124	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1	PGCIL	10/2011	11/2013	02/2016	558.26	27
125	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	PGCIL	09/2011	09/2014	06/2016	1940.13	21
126	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	09/2019	1657	43

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
127	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	11/2015	487.49	17
128	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHHATTISGARH	PGCIL	11/2011	07/2014	06/2016	2127.51	23
129	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	05/2016	573.99	33
130	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED	PGCIL	12/2011	02/2014	12/2015	552.44	22
131	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	02/2016	297.33	18
132	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	03/2012	06/2015	06/2016	9569.76	12
133	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV	PGCIL	11/2011	11/2014	06/2016	723.63	19
134	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B	PGCIL	02/2012	10/2014	06/2016	3201.44	20
135	SOLAPUR STPP	NTPC	03/2012	11/2016	08/2017	9395.18	9
136	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII	PGCIL	09/2012	05/2015	01/2016	524.4	8
137	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B	PGCIL	03/2013	12/2015	12/2016	2514.88	12
138	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C	PGCIL	03/2013	06/2015	08/2016	514.2	14

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
139	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE	MRTP	04/2012	04/2016	03/2017	714.1	11
140	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	MRTP	04/2008	03/2014	03/2019	5300	60
141	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	03/2016	1676.31	84
142	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2018	813.34	48
143	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	51
144	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2018	2500	193
145	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	03/2017	325	84
146	GONDIA-JABALPUR (GC), (SECR)	SECR	02/1997	03/1998	12/2019	386.3	261
147	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	12/2019	293.97	174
148	RANCHI-LOHARDAGA (GC), SER	SER	04/1997	06/2004	12/2015	194.07	138

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
149	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	03/2016	171.1	48
150	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2018	619.34	47
151	KATAKHAL TO BHAIRABI	NFR	04/1998	12/2012	03/2016	227.9	39
152	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP)	M RTP	03/1996	03/2004	03/2016	495.44	144
153	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2017	1500	110
154	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	03/2018	733	111
155	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	NFR	04/2003	03/2011	03/2019	727.56	96
156	PATNA GANGA BRIDGE (NL), ECR	ECR	04/2001	10/2007	12/2015	624.47	98
157	NEW LINE FROM DIMAPUR TO ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2020	850	60
158	KATIHAR - JOGBANI (GC) (NEFR)	NFR	09/2001	12/2010	03/2018	492.98	87
159	BANKURA - DAMODAR (GC) (SER)	SER	03/1998	03/2005	12/2019	111.9	177
160	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	12/2015	687.2	69
161	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	M RTP	03/2013	03/2016	06/2018	4874.58	27
162	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	03/2007	03/2016	895	108
163	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION	SER	04/2010	03/2015	12/2016	149.9	21

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
164	NALBARI TO BIJNI (AS-6)	NHAI	12/2003	06/2008	04/2016	225	94
165	NALBARI T BIJNI (AS-7)	NHAI	12/2003	04/2008	01/2017	208	105
166	SONAPUR TO GUWAHTI (AS-3)	NHAI	12/2003	03/2008	04/2016	245	97
167	GUWAHATI TO NALBARI (AS-5)	NHAI	12/2003	04/2008	12/2015	198.16	92
168	REHABILITATION & UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) T	PWD	02/2014	07/2014	07/2016	258.99	24
169	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	NHAI	12/2003	05/2008	12/2015	160	91

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
170	GUWHATI TO NALBARI (AS-4)	NHAI	12/2003	04/2008	12/2015	175.96	92
171	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC	PWD	07/2014	02/2015	02/2017	251.55	24
172	BRAHMPUTRA BRIDGE, NH NO-31	NHAI	12/2003	04/2010	02/2016	217.61	70

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
173	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT TR	01/2007	12/2010	01/2016	366.39	61
174	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL	MUMBAI PORT TR	11/2007	12/2010	09/2017	1228	81
175	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	03/2007	04/2009	08/2016	245.67	88
176	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	12/2015	150	117

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
177	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B	SAIL	11/2012	06/2015	12/2015	313.05	6
178	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES	SAIL	12/2011	10/2013	03/2016	187.33	29
179	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS	RINL	07/2011	07/2015	06/2016	877.73	11
180	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	12/2016	15525	19
181	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP	SAIL	10/2012	09/2014	12/2015	160.48	15
182	EXPANSION OF BHILAI STEEL PLANT	SAIL	08/2010	03/2013	06/2016	17265	39
183	SMS-1 CONVERTERS REVAMPING	RINL	05/2012	07/2015	03/2017	404.16	20
184	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA	SAIL	06/2012	12/2014	01/2016	237.09	13
185	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH	SAIL	07/2012	08/2014	01/2016	332.65	17

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
186	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS	BSNL	10/2009	10/2010	11/2015	384	61

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
187	DELHI MRTS PHASE-III	DMRCL	09/2011	03/2016	12/2016	38585	9
188	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI	CPWD	05/2009	05/2013	06/2016	261.85	37
189	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	CPWD	02/2014	09/2015	12/2016	156.57	15
190	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL	CPWD	12/2012	12/2014	12/2016	188.87	24
191	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA	CPWD	01/2009	06/2012	12/2015	225.81	42
192	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	CPWD	11/2012	11/2014	03/2016	270.83	16
193	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI	CPWD	05/2012	12/2014	04/2016	405.01	16
194	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	01/2015	12/2015	23136	11
195	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	CPWD	07/2012	08/2014	01/2016	884.3	17
196	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	08/2016	14600	8

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

ATOMIC ENERGY								
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)	
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	5677	2185	
2	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	13171	22462	9291	
COAL								
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)	
3	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	259.4	486.57	227.17	
4	ADRIYALA SHAFT PROJECT	SCCL	12/2009	03/2013	212.34	1228.39	1016.05	
HEAVY INDUSTRY								
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)	
5	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	HIPE	04/2011	09/2011	1718	3827.3	2109.3	
PETROCHEMICALS								
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)	
6	ASSAM GAS CRACKER PROJECT	BCPL	04/2006	04/2012	5460.61	9965	4504.39	
PETROLEUM								
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)	
7	INTEGRATED DEVELOPMENT OF BASSEIN FIELD	ONGC	12/2012	02/2016	3513.07	4619.94	1106.87	
8	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	607.06	714.25	107.19	
9	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	993	1693	700	
10	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	871.35	1200	328.65	
11	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	ISPRL	01/2006	10/2011	732	1227	495	
12	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	309.81	462.79	152.98	
13	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	666	838.08	172.08	
14	REWARI KANPUR PIPELINE PROJECT	HPCL	02/2012	11/2015	1210.64	1446.34	235.7	
15	INTEGRATED REFINERY EXPANSION PROJECT	BPCL	03/2012	05/2016	14225	16504	2279	
16	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	2059.63	2665.65	606.02	
17	PARADIP REFINERY PROJECT	IOCL	02/2009	11/2012	29777	34555	4778	

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
18	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT (MOPS)	ONGC	03/2011	05/2013	861.79	1256.72	394.93
19	GAMJI REDEVELOPMENT PROJECT	ONGC	05/2015	11/2019	1671.22	1881.22	210
20	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	4124.35	4941.49	817.14
21	MH NORTH REDEVELOPMENT PHASE III	ONGC	06/2014	05/2017	5706.47	5813.25	106.78
POWER							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
22	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	7818.68	3899.09
23	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	18063.89	11778.56
24	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	477.69	721.81	244.12
25	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	NHPC	09/2005	09/2009	1061.38	1929.15	867.77
26	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	421.01	1007.57	586.56
27	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	368.72	1381.71	1012.99
28	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	8692.97	15095.67	6402.7
29	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	1746.65	2228.71	482.06
30	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	573.99	1487.49	913.5
31	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	487.49	639.46	151.97
32	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	1657	2978.86	1321.86
33	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	2496.9	6476.34	3979.44
34	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	DVC	04/2007	02/2011	4122	9606.82	5484.82
35	BOKARO THERMAL POWER STATION-A	DVC	08/2006	12/2011	2313	4237.67	1924.67
36	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	4375.35	6749.18	2373.83
37	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	3846.3	867.82
38	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	1779.29	2159.07	379.78

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
39	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	3642.04	5497.72	1855.68
40	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A	PGCIL	09/2010	03/2013	2074.86	2348.37	273.51
41	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	11130.19	13762.8	2632.61
RAILWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
42	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	NCR	04/1986	03/1994	158.77	608.02	449.25
43	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR	NFR	04/1983	N.A.	36.8	1336.57	1299.77
44	CALICUT-MANGALORE (DL) (SR)	SR	02/1996	N.A.	240	579.37	339.37
45	KARUR-SALEM(NL), SR	SR	02/1997	N.A.	155.55	800	644.45
46	KATIHAR - JOGBANI (GC) (NEFR)	NFR	09/2001	12/2010	492.98	1727.27	1234.29
47	GULBARGA-BIDAR, SCR(NL)	SCR	02/1998	N.A.	242.42	844	601.58
48	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR) (GC)	SR	03/1998	N.A.	280	1122	842
49	KOTLIPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	N.A.	330	1047	717
50	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT (MTP)	M RTP	03/2000	12/2006	1049.69	3404.92	2355.23
51	GADWAL - RAICHUR (NL), SCR	SCR	04/1998	02/2011	92.63	270	177.37
52	BANKURA - DAMODAR (GC) (SER)	SER	03/1998	03/2005	111.9	2371.85	2259.95
53	JIND-SONEPAT (NL), NR	NR	01/2004	03/2012	238.56	740	501.44
54	HARIDASPUR-PARADEEP (NL)	RVNL	04/1996	N.A.	301.64	1185.64	884
55	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR	ECR	04/2002	03/2009	921	2363	1442
56	TUMKUR-CHITRADURGA-DAVENGERE NL	SWR	04/2011	N.A.	913	1801.01	888.01
57	PANVEL PEN DOUBLING	CR	04/2006	N.A.	96.16	260.16	164
58	PEN ROHA DOUBLING	CR	04/2007	N.A.	98.74	203	104.26
59	WARDHA-NANDED MAHARASHTRA	CR	04/2008	N.A.	499.3	2501.05	2001.75
60	KATAKHAL TO BHAI RABI	NFR	04/1998	12/2012	227.9	331.4	103.5

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
61	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2012	603.04	1421.25	818.21
62	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	03/2008	743	1117.11	374.11
63	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	N.A.	378.56	791.59	413.03
64	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	171.1	275.08	103.98
65	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	1500	4996.19	3496.19
66	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP)	M RTP	03/1996	03/2004	495.44	1781.98	1286.54
67	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	N.A.	514.68	2820	2305.32
68	MM FROM PANSKURA-GHATAL NL	SER	04/2011	01/1999	276.69	426	149.31
69	MM FROM BURAMARA-CHAKULIA	SER	04/2008	01/1999	466.48	800	333.52
70	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI	SR	04/1999	01/1999	460.94	1030	569.06
71	GADAG-WADI NL	SWR	04/2013	N.A.	1117	1922	805
72	HARIDWAR-LAKSAR	NR	04/2012	N.A.	219.83	329.97	110.14
73	RAYADURGA-TUMKUR NL	SWR	04/2007	N.A.	970.34	1743	772.66
74	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	4190	2850.52
75	KISHANGANJ JALALGARH, NL, NEFR	NFR	04/2008	N.A.	282.92	565.13	282.21
76	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	813.34	2876	2062.66
77	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	1676.31	5500	3823.69
78	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	5300	7986.04	2686.04
79	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	850	2973.42	2123.42
80	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	N.A.	300	827.73	527.73
81	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	N.A.	200	496.24	296.24
82	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	NFR	12/2006	03/2011	170	485	315
83	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	N.A.	601.43	800	198.57

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
84	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	M RTP	04/2012	03/2016	632.68	816.55	183.87
85	LUMDING-HOJAI PATCH DOUBLING PROJECT	NFR	04/2012	N.A.	246.07	364.06	117.99
86	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	N.A.	312.12	453.1	140.98
87	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI	NFR	04/1999	N.A.	523.17	1653.55	1130.38
88	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	N.A.	165.82	435.58	269.76
89	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	394.28	152.76
90	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	N.A.	242.22	679.57	437.35
91	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	N.A.	4083.02	5307.9	1224.88
92	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	SR	04/2007	N.A.	247	951.24	704.24
93	MADURAI-BODINAYAKKANUR	SR	04/2008	N.A.	164.41	450	285.59
94	ERODE-PALANI	SR	04/2008	N.A.	288.57	603.22	314.65
95	NEW COOCHBEHAR TO SAMUKTALA	NFR	04/2011	N.A.	209.77	441.45	231.68
96	DIMAPUR-TIZIT NL	NFR	04/2013	N.A.	4274	4487.7	213.7
97	AGARTALA-AKHAURA NL	NFR	04/2012	N.A.	252	886.65	634.65
98	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	03/2007	895	1242.25	347.25
99	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	NFR	04/2010	N.A.	221.42	563.13	341.71
100	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	SR	04/2008	N.A.	822.39	1280.83	458.44
101	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	SR	04/1998	N.A.	271.24	520	248.76
102	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	SR	04/1999	N.A.	198.68	556.64	357.96
103	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	SR	04/2013	N.A.	839	1500	661
104	CHENNAI-CUDDALORE VIA MAMALLAPURAM	SR	04/2008	N.A.	523.52	1200	676.48
105	HAJIPUR-RAMDAYALUNAGAR DOUBLING	ECR	04/2013	N.A.	213.01	367.17	154.16
106	MOTIHARI-SITAMARHI (NL)	ECR	04/2006	N.A.	211	926.09	715.09

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
107	SAKRI-HASANPUR ROAD (NL)	ECOR	04/1999	N.A.	175.69	325	149.31
108	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	N.A.	258.2	365	106.8
109	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	12/2015	309.44	583	273.56
110	BHADUTOLA-JHARGRAM VIA LALGARH (NL)	SER	04/2011	N.A.	289.64	760	470.36
111	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	N.A.	553.63	1009	455.37
112	BOWAICHANDI-ARAMBAGH	SER	04/2010	N.A.	267.37	434	166.63
113	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR	NCR	04/2010	02/2019	622.41	2030.5	1408.09
114	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	NWR	04/2010	N.A.	739.65	872.22	132.57
115	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTURGARH-UDAIPUR	NWR	04/2013	N.A.	456	855.16	399.16
116	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	1176.09	3845.6	2669.51
117	RATLAM-DUNGARPUR VIA BANSWARA (NL)	NWR	04/2011	N.A.	2082.75	3500	1417.25
118	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	N.A.	446	685.17	239.17
119	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	N.A.	320.66	913.48	592.82
120	CHHAPRA-BALLIA UP	NER	03/2013	N.A.	295	494.92	199.92
121	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	N.A.	826.57	1143.6	317.03
122	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	N.A.	679.27	1111.99	432.72
123	BANGLORE - SATYAMANGALAM (NL) (SWR)	SWR	04/1996	N.A.	138	1382.78	1244.78
124	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA (NL) , SWR	SWR	02/1997	N.A.	295	1289.92	994.92
125	HUBLI-ANKOLA (NL) , SWR	SWR	04/1997	N.A.	227	2135	1908
126	RANCHI-LOHARDAGA (GC) , SER	SER	04/1997	06/2004	194.07	335	140.93
127	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	293.97	1428	1134.03
128	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	393.46	1026	632.54
129	GONDIA-JABALPUR (GC) , (SECR)	SECR	02/1997	03/1998	386.3	1544.4	1158.1

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
130	MACHERLA-NALGONDA (NL) (SCR)	SCR	07/1998	07/2008	125	480	355
131	MUNEERABAD-MAHABOONNAGAR (NL) , SCR	SCR	04/1997	N.A.	218.24	645	426.76
132	ANGAMALI-SABARIMALA (N.L.) (SR)	SR	10/1998	N.A.	550	1566	1016
133	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL (SCR)	SCR	12/1994	N.A.	124.43	925.3	800.87
134	TIRUCHIRAPPALI-NAGORE-KARAIKKAL (SR) (GC)	SR	09/1995	N.A.	100	980	880
135	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	SWR	04/2007	03/2013	482	874.57	392.57
136	NANDYAL-YERRAGUNTALA (NL) , SCR	SCR	03/1996	02/2009	155.74	883	727.26
137	RAJATGARH-BARANG (LD) , ECOR	RVNL	04/1999	02/2009	166.16	288	121.84
138	DALLI-RAJHARA - RAOGHAT (PART OF DALLI-RAJHARA-JAGDALPUR) , NL, RVNL	RVNL	04/1995	12/2012	304	968.6	664.6
139	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	325	1564.54	1239.54
140	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD) , NR	NR	03/2002	06/2007	625.3	847.75	222.45
141	UDHAMPUR-SRINAGAR-BARAMULLA (NL) , NR	NR	03/1995	11/2002	2500	19565	17065
142	NANGALDAM-TALWARA (NL) , NR	NR	03/1981	07/2012	450	2100	1650
143	KANPUR-KASGANJ-MATHURA (GC) , NER	NER	03/1997	N.A.	677.97	1651.54	973.57
144	PATNA GANGA BRIDGE (NL) , ECR	ECR	04/2001	10/2007	624.47	2921	2296.53
145	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	NFR	04/2003	03/2011	727.56	6570.75	5843.19
146	KHURDA ROAD-BOLANGIR (NL) ECOR	ECOR	04/1994	N.A.	470.21	1995.25	1525.04
147	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) , NEFR	NFR	04/2000	12/2008	733	2531.34	1798.34
148	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	541	378.13
149	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	12/2009	108	432.72	324.72
150	JAYANAGAR-DARBHANGA-NARKATIA GANJ (GC) , ECR	ECR	04/1997	03/2012	501.69	1043.56	541.87
151	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	1630.97	1383.31
152	SHIMOGA-HARIHAR NL	SWR	04/2011	N.A.	562.74	832.47	269.73

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
153	SRINIVASA-PURA-MADANAPALLI NL	SWR	04/2013	N.A.	296	466.65	170.65
154	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	SWR	04/2013	N.A.	558	692.43	134.43
155	BHANUPALI-BILASPUR BERI NL	NR	04/2008	N.A.	1046.88	2966.99	1920.11
156	ROHTAK-MEHAM HANSI	NR	04/2012	N.A.	287	576.18	289.18
157	AKOLA-KHANDWA GC AKOLA-AKOT	SCR	04/2008	N.A.	184.26	2000	1815.74
158	BAGALKOT-KUDACHI NL	SWR	04/2010	N.A.	377.93	986.3	608.37
159	MUNIRABAD (GINGERA) -RAICHUR NL	SWR	04/2007	N.A.	179.65	1350.91	1171.26
160	TIDIVANAM-NAGARI (NL)	SR	09/2006	N.A.	456	1080	624
161	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	SR	09/2006	N.A.	125	490	365
162	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	SR	09/2006	N.A.	343.17	914.98	571.81
163	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	SR	09/2007	N.A.	404.19	1383.45	979.26
164	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	687.2	800	112.8
165	RAICHUR-GUNTAKAL (DL) (SCR)	RVNL	04/2003	12/2007	136.62	289.93	153.31
166	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	133.41	276	142.59
167	SUKINDA ROAD - ANGUL (NL) (ECOR)	RVNL	04/1998	02/2015	183.23	818.29	635.06
168	VIRAMGAM-BHILDI (WR), GC	WR	04/1990	N.A.	155.66	548.01	392.35
169	MANSI-PURNIA (EXTENSION OF MANSI- SAHARSA) GAN ECR	ECR	04/1996	03/2012	332.92	477.88	144.96
170	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	619.34	2820.25	2200.91
171	CHHINDWARA - NAGPUR (GC) (SECR)	SECR	04/2005	N.A.	383.79	1101.16	717.37
172	ETAWAH-MAINPURI (NL), NCR	NCR	04/1997	12/2008	120	245.39	125.39
173	MAHARAJGANJ-MASRAKH (NL) - NER	NER	04/2003	N.A.	218.19	343	124.81
174	RAMGANJMUNDI-BHOPAL (NL), WCR	WCR	04/2001	N.A.	470.92	1225.9	754.98

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

ROAD TRANSPORT AND HIGHWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
175	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	199.81	385.13	185.32
176	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S	PWD	03/2011	12/2015	218.31	339.82	121.51
177	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	155.04	280.13	125.09
178	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	1108	2288	1180
179	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	196	331.23	135.23
SHIPPING AND PORTS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
180	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL	MUMBAI PORT	11/2007	12/2010	1228	1460	232
181	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT	01/2007	12/2010	366.39	669.46	303.07
182	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	150	600	450
183	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	03/2007	04/2009	245.67	409.83	164.16
STEEL							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
184	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	343	488.4	145.4
URBAN DEVELOPMENT							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
185	BANGALORE METRO RAIL PROJECT	M RTP	05/2006	06/2011	6395	11609	5214

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	06/2016	1,3171.00	2,2462.00	9291	90
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	09/2016	3492.00	5677.00	2185	72

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
3	ADRIYALA SHAFT PROJECT	SCCL	12/2009	03/2013	03/2016	212.34	1228.39	1016.05	36
4	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	03/2017	259.40	486.57	227.17	60

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
5	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	HIPE	04/2011	09/2011	12/2017	1718.00	3827.30	2109.3	75

PETROCHEMICALS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
6	ASSAM GAS CRACKER PROJECT	BCPL	04/2006	04/2012	12/2015	5460.61	9965.00	4504.39	44

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
7	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	08/2016	871.35	1200.00	328.65	17
8	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	ISPRL	01/2006	10/2011	03/2016	732.00	1227.00	495	53
9	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	12/2017	4124.35	4941.49	817.14	20
10	INTEGRATED DEVELOPMENT OF BASSEIN FIELD	ONGC	12/2012	02/2016	12/2017	3513.07	4619.94	1106.87	22
11	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	03/2016	993.00	1693.00	700	50
12	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	03/2017	309.81	462.79	152.98	29

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
13	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT (MOPS)	ONGC	03/2011	05/2013	04/2016	861.79	1256.72	394.93	35
14	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	05/2016	2059.63	2665.65	606.02	14
15	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	11/2016	666.00	838.08	172.08	12
16	PARADIP REFINERY PROJECT	IOCL	02/2009	11/2012	01/2016	2,9777.00	3,4555.00	4778	38

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
17	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	12/2015	421.01	1007.57	586.56	29
18	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	11/2015	487.49	639.46	151.97	17
19	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2018	2978.48	3846.30	867.82	69
20	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	03/2017	4375.35	6749.18	2373.83	66
21	BOKARO THERMAL POWER STATION-A	DVC	08/2006	12/2011	03/2016	2313.00	4237.67	1924.67	51
22	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	DVC	04/2007	02/2011	01/2017	4122.00	9606.82	5484.82	71
23	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	12/2016	2496.90	6476.34	3979.44	84
24	TEHRI PUMPED STORAGE PLANT (1000MW)	THDCIL	07/2006	02/2016	09/2019	1657.00	2978.86	1321.86	43
25	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	05/2016	573.99	1487.49	913.5	33
26	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	06/2016	1746.65	2228.71	482.06	22
27	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2018	3919.59	7818.68	3899.09	111
28	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	NHPC	09/2005	09/2009	06/2016	1061.38	1929.15	867.77	81

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
29	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	06/2016	477.69	721.81	244.12	69
30	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A	PGCIL	09/2010	03/2013	01/2016	2074.86	2348.37	273.51	34
31	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	12/2017	1,1130.19	1,3762.80	2632.61	52
32	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	10/2017	368.72	1381.71	1012.99	135
33	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	05/2018	8692.97	1,5095.67	6402.7	88
34	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	11/2016	3642.04	5497.72	1855.68	10
35	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	12/2016	1779.29	2159.07	379.78	97

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
36	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	03/2007	03/2016	895.00	1242.25	347.25	108
37	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	03/2017	325.00	1564.54	1239.54	84
38	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	4190.00	2850.52	51
39	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	03/2016	1676.31	5500.00	3823.69	84
40	KATAKHAL TO BHAIRABI	NFR	04/1998	12/2012	03/2016	227.90	331.40	103.5	39
41	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP)	MRTP	03/1996	03/2004	03/2016	495.44	1781.98	1286.54	144
42	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2017	1500.00	4996.19	3496.19	110
43	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	03/2018	733.00	2531.34	1798.34	111
44	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	NFR	04/2003	03/2011	03/2019	727.56	6570.75	5843.19	96

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
45	PATNA GANGA BRIDGE (NL), ECR	ECR	04/2001	10/2007	12/2015	624.47	2921.00	2296.53	98
46	NEW LINE FROM DIMAPUR TO ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2020	850.00	2973.42	2123.42	60
47	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	03/2019	5300.00	7986.04	2686.04	60
48	KATI HAR - JOGBANI (GC) (NEFR)	NFR	09/2001	12/2010	03/2018	492.98	1727.27	1234.29	87
49	BANKURA - DAMODAR (GC) (SER)	SER	03/1998	03/2005	12/2019	111.90	2371.85	2259.95	177
50	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	12/2015	687.20	800.00	112.8	69
51	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	03/2016	171.10	275.08	103.98	48
52	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2018	619.34	2820.25	2200.91	47
53	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2018	813.34	2876.00	2062.66	48
54	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2018	2500.00	1,9565.00	17065	193
55	GONDIA-JABALPUR (GC), (SECR)	SECR	02/1997	03/1998	12/2019	386.30	1544.40	1158.1	261
56	RANCHI-LOHARDAGA (GC), SER	SER	04/1997	06/2004	12/2015	194.07	335.00	140.93	138
57	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	12/2019	293.97	1428.00	1134.03	174

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
58	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT TRU	01/2007	12/2010	01/2016	366.39	669.46	303.07	61
59	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL	MUMBAI PORT TRU	11/2007	12/2010	09/2017	1228.00	1460.00	232	81
60	ENORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	12/2015	150.00	600.00	450	117

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipa ted	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
61	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	03/2007	04/2009	08/2016	245.67	409.83	164.16	88

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun
