

384th
FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(Rs.150 crore and above)
October 2017



PORT TRUST - SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India Ltd.
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead Travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised Catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Operation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petroleum Corporation Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative Ltd.
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation Ltd.
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Corporation.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Corporation.
NCL	Northern Coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation Ltd.
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corporation Ltd.
NGN	Next Generation Network
NLC	Neyveli Lignite Corporation Ltd.
NMDC	National Mineral Development Corporation Ltd.
NPC	Nuclear Power Corporation Ltd.
NRL	Numaligarh Refinery Ltd.
OB	Over Burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over Bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India Ltd.
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

EXECUTIVE SUMMARY

1. The Flash Report for October 2017 contains information on the status of the 1283 Central Sector Infrastructure Projects costing ₹ 150 crore and above.

2. The implementation status of **Central Sector Projects (costing Rs 150 crore and above)** may be summarized as below:-

(i). During the reference month, 42 projects have reported additional delays vis-à-vis their date of completion reported in the previous month. Of these 42 projects, 25 are **Mega** Projects costing ₹ 1000 crore and above.

(ii). Total original cost of implementation of the 1283 projects was Rs.15,58,352.33 crore and their anticipated completion cost is likely to be Rs.17,59,443.87 crore, which reflects overall cost overruns of Rs.2,01,091.54 crore (12.90% of original cost). The expenditure incurred on these projects till October 2017 is Rs.6,59,009.46 crore, which is 37.46% of the anticipated cost of the projects.

(iii). Out of a total of 1283 projects, 12 projects have reported completion and 34 new projects have been initiated on the monitor of this ministry during the current month. Of these, 13 projects are ahead of schedule, 317 are on schedule, 302 are delayed, 349 projects are showing cost overrun and 105 projects are showing both time and cost overrun with respect to original implementation schedules. However, the number of delayed projects decreases to 258 if delay is calculated with reference to latest revised schedules of completion. For 651 projects, where original/anticipated commissioning date has not been reported, all concerned have been requested to provide the original/anticipated commissioning date so that these projects can be monitored for completion vis-a-vis the targeted dates.

(iv). Out of 302 delayed projects, 49 projects have overall delay in the range of 1 to 12 months, 66 projects have delay in the range of 13 to 24 months, 108 projects have delay in the range of 25 to 60 months and 79 projects have delay of 61 months and above.

(v). Further, out of the 302 delayed projects, 105 projects have cost overruns. Out of these, the cost for 53 projects has been revised and for 52 projects the cost has not yet been revised. Of the 53 projects where cost has been revised, the anticipated cost of 9 projects has again exceeded the revised cost. Out of 302 delayed projects, 160 projects have not provided any milestones and in 99 cases the dates of completion of the milestones have already lapsed.

(vi). In addition to above there are 244 projects which though on schedule but are having cost overruns. Of these, the cost for 59 projects has since been revised. Of the 59 projects where cost has been revised, the anticipated cost of 25 projects has exceeded even the revised costs. Out of these 244 projects, 163 projects have not provided any milestones and for 4 projects the completion date of milestone(s) has already lapsed.

(vii). In the current month, there are 290 projects showing time overrun of more than 6 months; 253 projects showing cost overruns of more than Rs.100 crore and 87 projects showing both time overruns of more than 6 months and cost overruns of more than Rs.100 crore. Further, expenditure has exceeded the approved cost in 151 projects and in 941 projects milestones have not been reported. Concerned secretaries have been requested to take a review of these projects to fix time lines and cost estimates.

3. The implementation status of **Central Sector Mega Projects** (costing Rs.1000 crore and above) may be summaries as below:-

(i) During the reference month out of 1283 projects 382 are mega projects. Total original cost of implementation of these 382 projects was Rs.11,92,573.37 crore and their anticipated completion cost is likely to be Rs.13,64,584.39 crore, which reflects overall cost overruns of Rs.1,72,011.02 crore (14.42% of original cost). The expenditure incurred on these projects till October 2017 is Rs. 5,44,206.92 crore, which is 39.88% of the anticipated cost of the projects. Out of the 382 mega projects, 144 projects have cost overruns with respect to original cost and the number of such projects decreases to 115 when cost overrun is calculated on the basis of revised cost.

(ii) Further, out of the 129 delayed mega projects, 56 projects have cost overruns. Out of these, the cost for 26 projects has been revised and for 30 projects the cost has not yet been revised. Of the 26 projects where cost has been revised, the anticipated cost of 5 projects has again exceeded the revised cost. Out of 129 delayed projects, 67 projects have not provided any milestones and in 50 cases the dates of completion of the milestones have already lapsed.

(iii) In addition to above there are 88 mega projects which though are on schedule but are having cost overruns. Of these, the cost for 20 projects has since been revised and for 68 projects cost has not been revised. Of the 20 projects where cost has been revised, the anticipated cost of 11 projects has exceeded even the revised costs. Out of these 88 projects, 56 projects have not provided any milestones and for 1 project the completion date of milestone(s) has already lapsed.

(iv). In the current month, there are 121 mega projects showing time overruns of more than 6 months; 135 mega projects showing cost overruns of more than Rs.100 crore and 55 mega projects showing both time overruns of more than 6 months and cost overruns of more than Rs.100 crore.

Further, expenditure has exceeded the approved cost in 65 mega projects and in 263 mega projects milestones have not been reported. Concerned secretaries have been requested to take a review of these projects to fix time lines and cost estimate.

4. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in forest clearance, delay in supply of equipments, fund constraints, geological surprises, problems in equipment erection, geo-mining conditions, slow progress in civil works, shortage of labour, inadequate mobilization by the contractor, maoist problems, court cases, contractual issues, ROU/ROW problems, law and order situation etc.

5. The Online Computerized Monitoring System (OCMS) of this Ministry envisages monitoring of milestones of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones.

6. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported.

7. Ministry of Railways have provided the latest information of all its ongoing projects costing ₹500 crore and above on the OCMS of this Ministry. The recent and latest updated information in respect of projects costing below ₹500 crore is reported as and when received.

8. The status as on 31.10.2017 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report available at [www.cspm.gov.in /publication](http://www.cspm.gov.in/publication).

9. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

TABLE-1

EXECUTIVE SUMMARY COSTING Rs.150 crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	495	5
2	RAILWAYS	350	4
3	POWER	126	17
4	PETROLEUM	109	3
5	COAL	91	2
6	URBAN DEVELOPMENT	34	1
7	STEEL	32	4
8	HEALTH AND FAMILY WELFARE	16	3
9	SHIPPING AND PORTS	8	0
10	TELECOMMUNICATIONS	8	1
11	MINES	4	0
12	ATOMIC ENERGY	3	1
13	CIVIL AVIATION	2	1
14	FERTILISERS	2	0
15	DEFENCE PRODUCTION	2	0
16	HEAVY INDUSTRY	1	0
	Total	1283	42

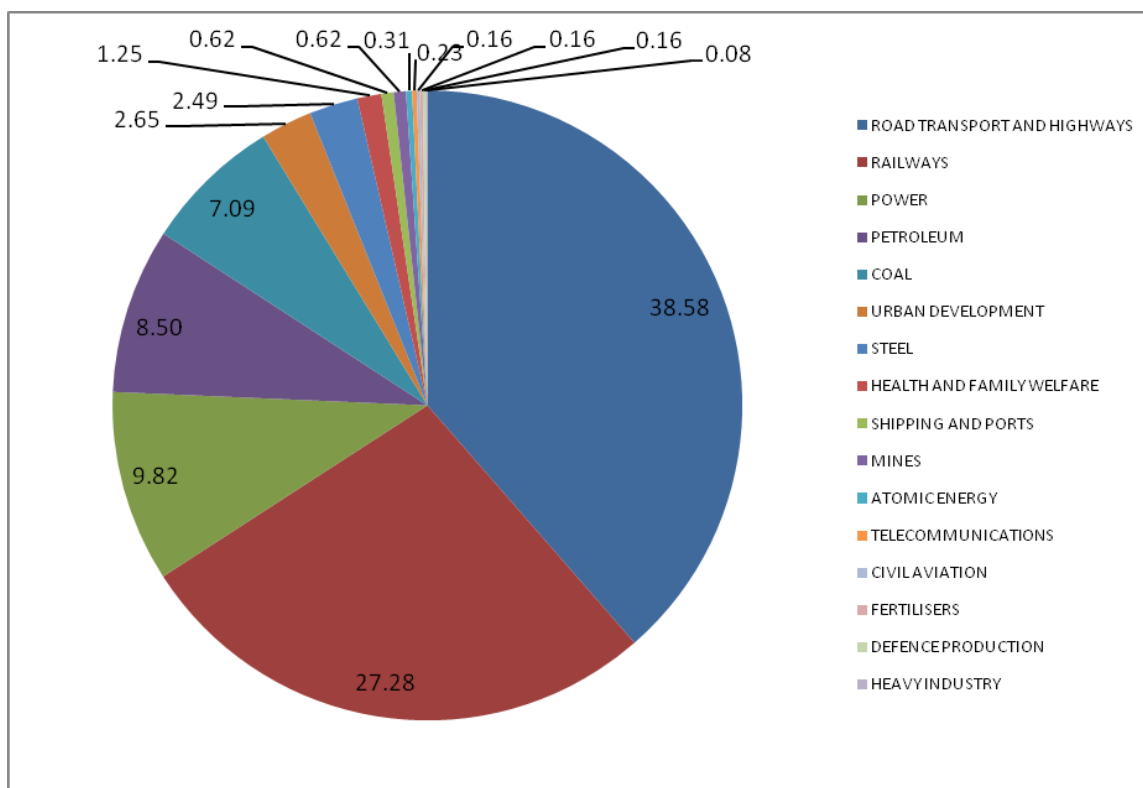


TABLE-2

Month wise List of Completed Projects Costing Rs.150 crore and above during				
2017-2018				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2017			
	<u>PETROCHEMICALS</u>			
1	ASSAM GAS CRACKER PROJECT G(BRAHMAPUTRA CRECKER & POLYMER LTD.) - [N16000106]	5,460.61	04/2012	9,895.05
	<u>POWER</u>			
2	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000053]	509.66	11/2011	566.26
3	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000081]	1,216.83	08/2012	1,074.89
4	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000101]	1,961.87	05/2014	1,817.05
5	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000117]	1,422.85	01/2015	1,490.42
6	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000145]	1,909.24	06/2015	1,093.03
7	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000163]	303.07	07/2016	48.50
8	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000173]	972.42	11/2017	92.20
	May,2017			
	<u>CIVIL AVIATION</u>			
9	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS G(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000071]	217.60	03/2015	196.94
	June,2017			
	<u>STEEL</u>			
10	SMS-1 CONVERTERS REVAMPING G(RASTRIYA ISPAT NIGAM LIMITED) - [N12000090]	404.16	07/2015	394.74
	<u>POWER</u>			
11	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000166]	378.71	10/2016	257.90
12	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000167]	400.47	04/2017	265.20

Month wise List of Completed Projects Costing Rs.150 crore and above during

2017-2018

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
13	TRANSMISSION SYSTEM ASSOCIATED WITH DARLIPALLI TPS G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000211]	187.04	06/2018	54.60
	July,2017			
14	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000094]	752.64	07/2013	633.62
15	WARDHA-HYDERABAD 765 KV LINK G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000183]	3,662.02	05/2018	2,302.40
	August,2017			
16	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000153]	1,575.30	05/2016	1,328.51
	September,2017			
	<u>ATOMIC ENERGY</u>			
17	KUDANKULAM APP (NPCIL) G(NUCLEAR POWER CORPORATION OF INDIA LIMITED) - [020100040]	13,171.00	12/2008	22,340.00
	<u>CIVIL AVIATION</u>			
18	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) G(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000069]	335.61	05/2012	305.59
	<u>PETROLEUM</u>			
19	DE-BOTTLENECKING OF SMPL G(INDIAN OIL CORPORATION LIMITED) - [N16000089]	1,584.00	03/2017	1,355.45
20	INTEGRATED REFINERY EXPANSION PROJECT G(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000143]	16,504.00	03/2017	15,090.99
21	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) G(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000146]	666.00	11/2015	606.13
22	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE G(INDIAN OIL CORPORATION LIMITED) - [N16000149]	586.00	08/2015	440.20
23	MARKETING TOP AT KORBA G(INDIAN OIL CORPORATION LIMITED) - [N16000186]	141.86	09/2016	174.37
24	INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND ASSOCIATED FACILITIES G(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000205]	1,714.00	06/2017	1,067.89
	<u>POWER</u>			
25	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000112]	2,127.51	07/2014	2,582.69
26	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000125]	9,569.76	06/2015	7,311.17
27	KBUNL-MUZAFFARPUR TPP STAGE-II- SUBSIDIARY (2X195 MW) G(NATIONAL THERMAL POWER CORPORATION) - [N18000191]	3,984.03	01/2013	3,290.44
	October,2017			

Month wise List of Completed Projects Costing Rs.150 crore and above during

2017-2018

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	<u>COAL</u>			
28	WIND POWER PROJECT, KAZHUNEERKULAM, TAMILNADU G(NEYVELI LIGNITE CORPORATION) - [N06000110]	364.75	10/2014	333.05
	<u>STEEL</u>			
29	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS G(RASTRIYA ISPAT NIGAM LIMITED) - [N12000089]	877.73	07/2015	747.81
30	TURBO BLOWER - 5 G(RASTRIYA ISPAT NIGAM LIMITED) - [N12000092]	280.00	09/2016	157.09
	<u>PETROLEUM</u>			
31	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY G(INDIAN OIL CORPORATION LIMITED) - [N16000180]	163.88	07/2016	82.45
32	50 MW 10 PERCENT WIND ENERGY POWER PROJECT Central Sector Projects(OIL INDIA LIMITED) - [N16000208]	500.00	03/2017	368.24
33	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT) G(INDIAN OIL CORPORATION LIMITED) - [N16000217]	150.00	07/2014	251.90
	<u>RAILWAYS</u>			
34	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR G(SOUTH WESTERN RAILWAY) - [220100183]	295.00	-	1,509.88
35	GURIYA-MARWAR AND KARJODA-PALANPUR G(NORTH WESTERN RAILWAY) - [N22000154]	239.73	-	195.42
36	HOSADURGA - CHICKJAJUR (28.89 KM) G(SOUTH WESTERN RAILWAY) - [N22000324]	203.40	-	282.69
	<u>URBAN DEVELOPMENT</u>			
37	BANGALORE METRO RAIL PROJECT G(METROPOLITAN RAPID TRANSPORT PROJECTS) - [N28000008]	6,395.00	06/2011	14,200.11
38	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA G(CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000074]	315.00	06/2015	302.82
39	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI G(CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000077]	405.01	12/2014	349.54

TABLE-3

Month wise List of Deleted Projects Costing Rs.150 crore and above during				
2017-2018				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	July,2017			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
1	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000123]	940.00	07/2012	1,415.36
2	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000153]	359.00	09/2013	2.74
3	BHUBANESWAR TO PURI (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000195]	500.29	08/2013	869.91
4	4-LANING OF RAIGANJ-DALKOLA (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000204]	580.43	08/2013	226.67
5	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000225]	828.00	09/2014	870.15
6	2/4 LANING OF TALCHAR -DUBARI-CHANDIKHOLE SECTION OF NH-200 FROM KM 301.89 TO KM 427.85 INCLUDING KM(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000366]	996.37	12/2017	0.00
7	SIX LANE OF GREENFIELD PROPOSED UDAIPUR BYPASS [CONNECTION BETWEEN NH-76 AT EXISTING KM (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000588]	725.95	06/2019	0.00
	September,2017			
	<u>POWER</u>			
8	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI = II HEP (POWER GRID CORPORATION OF INDIA LIMITED) - [180100261]	358.42	12/2008	0.00
9	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000099]	1,585.12	11/2013	1,452.46
10	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000114]	552.44	02/2014	501.60
11	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000170]	188.75	02/2017	0.00
12	PATAN WIND FARM SITE, GUJARAT 50 MW (THDC INDIA LIMITED) - [N18000204]	315.00	10/2016	311.96
13	KANDORNA AND BHANWAD WIND FARM (THDC INDIA LIMITED) - [N18000234]	415.49	03/2017	415.50
	October,2017			
14	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM CUDDALORE AREA – PACKAGE A (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000259]	955.00	12/2015	74.00

Month wise List of Deleted Projects Costing Rs.150 crore and above during

2017-2018

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
15	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-A (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000260]	2,525.00	11/2017	564.00


Summary of projects in the Flash Report for the month of October, 2017

Project Implementation - Current Status:

Number of Projects in Previous Month	1263
Number of Projects completed/dropped/frozen in Current Month	14
	0
Number of Projects Added in Current Month	34
Number of Projects in Current Month	1283

Brief Analysis

Project Status with respect to Original Schedule: Out of 1283 projects, 13 projects are ahead of schedule, 317 projects are on schedule 302 projects are delayed. 516 projects do not have fixed dates of commissioning. 135 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

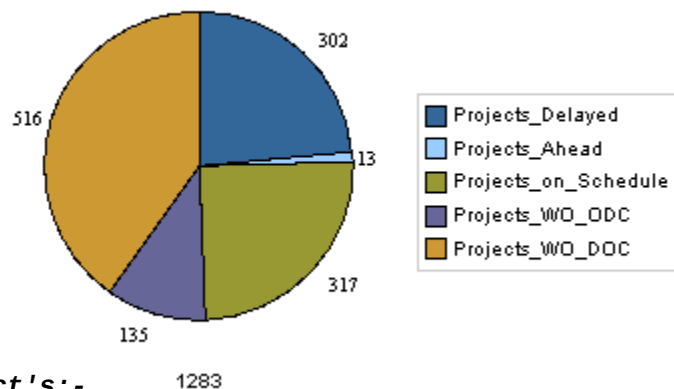

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1283 projects when sanctioned, was of the order of Rs. 1558352.33 crore but this was subsequently revised to Rs. 1759443.87 crore implying a cost overrun of 12.9%. The expenditure incurred on these projects till October, 2017 is Rs. 659009.46 crore, which is 37.5% of the anticipated cost of the projects.

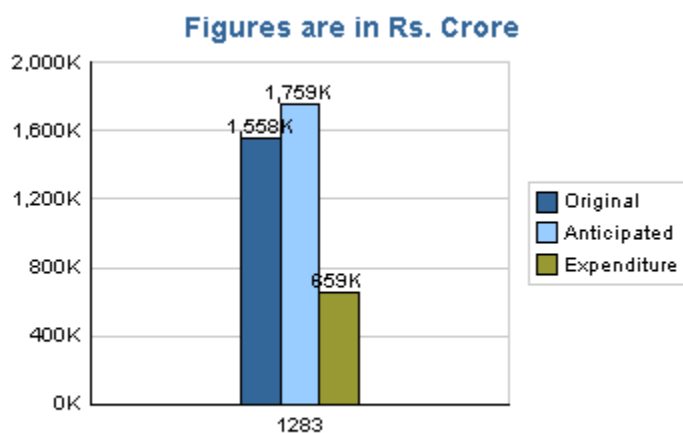


TABLE-4

Projects Added / Completed / Dropped / Frozen Rs.150 Crore and above

No of Projects in Previous Month	1263
No of Projects Completed/Dropped/Frozen in Current Month	14
No of Projects added in Current Month	34
No of Projects in Current Month	1283

Project status Rs. 150 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	302 (23.54%)	13 (1.01%)	317 (24.71%)	135 (10.52%)	516 (40.22%)	1283
Latest Approved (Date)	258 (20.11%)	11 (.86%)	366 (28.53%)	131 (10.21%)	517 (40.30%)	1283

Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	1130	13,65,457.93	14,75,534.70	4,86,016.51	32.90	1,10,076.77	8.10
Project with Revision in Cost	153	2,63,330.64	2,83,909.17	1,72,992.95	60.90	20,578.53	7.80
Total	1,283	16,28,788.57	17,59,443.87	6,59,009.46	37.46	1,30,655.30	8.02
Original Cost of All Projects							
Original Cost	1,283	15,58,352.33	17,59,443.87	6,59,009.46	37.46	2,01,091.54	12.90

Delayed Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	302	5,61,421.69	7,07,100.76	4,25,868.82	60.20	1,45,679.07	25.90
Latest Approved (RCE)	258	5,02,960.95	5,93,145.41	3,40,249.27	57.40	90,184.46	17.90

Additional Delayed Project cost Rs.150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	42	1,71,112.70	1,95,194.57	1,27,779.64	65.50	24,081.87	14.10

TABLE-5

Extent of cost overrun in projects with respect to original schedule(Sector Wise) Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun [^]			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	3	27,271.00	29,779.00	9.20	1	3,492.00	6,000.00	71.82
2	CIVIL AVIATION	2	624.07	994.86	59.41	2	624.07	994.86	59.41
3	COAL	91	87,760.24	88,310.52	0.63	9	19,751.90	21,154.17	7.10
4	FERTILISERS	2	680.64	703.44	3.35	2	680.64	703.44	3.35
5	MINES	4	6,773.63	6,773.63	0.00	0	0.00	0.00	0.00
6	STEEL	32	56,191.76	56,405.44	0.38	5	1,639.71	2,211.39	34.86
7	PETROLEUM	109	1,92,892.26	1,94,226.73	0.69	16	24,372.27	30,690.77	25.93
8	POWER	126	3,38,804.33	3,97,533.16	17.33	43	1,04,449.62	1,63,178.45	56.23
9	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
10	HEALTH AND FAMILY WELFARE	16	4,538.61	4,550.91	0.27	1	196.70	209.00	6.25
11	RAILWAYS	350	3,53,681.04	4,65,297.26	31.56	213	1,23,103.45	2,96,496.70	140.85
12	ROAD TRANSPORT AND HIGHWAYS	495	3,27,076.22	3,33,448.42	1.95	43	25,598.69	32,656.93	27.57
13	SHIPPING AND PORTS	8	4,117.75	5,085.02	23.49	5	1,205.50	2,172.77	80.24
14	TELECOMMUNICATIONS	8	16,776.04	28,006.04	66.94	1	13,334.00	24,664.00	84.97
15	URBAN DEVELOPMENT	34	1,38,993.10	1,44,033.10	3.63	5	16,524.82	21,745.20	31.59
16	DEFENCE PRODUCTION	2	453.64	469.04	3.39	2	453.64	469.04	3.39
Total		1283	15,58,352.33	17,59,443.87	12.90	349	3,37,145.01	6,07,174.02	80.09

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-6

Extent of cost overrun in projects with respect to original schedule (State Wise) Rs.150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun [^]			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	59	97,031.51	1,01,034.54	4.13	9	6,577.56	11,606.74	76.46
2	ARUNACHAL PRADESH	31	16,602.41	33,555.84	102.11	6	9,755.78	26,709.21	173.78
3	ASSAM	48	33,455.72	49,152.55	46.92	16	15,831.46	31,710.33	100.30
4	BIHAR	78	65,774.22	82,592.48	25.57	20	33,420.33	50,534.54	51.21
5	GOA	9	4,043.51	4,058.91	0.38	2	453.64	469.04	3.39
6	GUJARAT	44	39,186.12	41,822.49	6.73	10	5,641.30	9,568.61	69.62
7	HARYANA	21	14,081.22	15,967.45	13.40	3	1,633.56	3,653.00	123.62
8	HIMACHAL PRADESH	12	14,659.32	22,591.60	54.11	2	4,966.47	12,898.75	159.72
9	JAMMU AND KASHMIR	10	27,408.66	55,639.93	103.00	3	7,930.45	36,161.72	355.99
10	KARNATAKA	44	72,280.39	81,988.83	13.43	19	10,319.82	21,192.04	105.35
11	KERALA	21	21,774.25	27,871.82	28.00	7	3,017.36	9,114.93	202.08
12	MADHYA PRADESH	57	59,615.97	64,062.26	7.46	8	6,120.00	10,574.83	72.79
13	MAHARASHTRA	120	1,73,108.23	1,83,029.42	5.73	28	33,884.82	47,520.97	40.24
14	MANIPUR	2	944.25	9,874.69	945.77	1	727.56	9,658.00	1227.45
15	MEGHALAYA	6	7,108.02	9,025.00	26.97	1	4,083.02	6,000.00	46.95
16	MIZORAM	5	2,001.20	6,942.57	246.92	2	988.06	5,929.43	500.11
17	NAGALAND	7	8,126.79	10,276.79	26.46	1	850.00	3,000.00	252.94
18	ODISHA	68	72,862.34	80,530.99	10.52	19	6,641.38	14,326.32	115.71
19	PUNJAB	28	15,555.77	15,561.50	0.04	2	1,328.50	1,361.27	2.47
20	RAJASTHAN	62	44,731.54	47,002.58	5.08	14	5,767.37	8,038.41	39.38
21	SIKKIM	6	2,537.08	5,585.45	120.15	3	2,036.94	5,085.59	149.67
22	TAMIL NADU	61	67,331.87	82,216.33	22.11	21	27,563.13	43,196.70	56.72
23	TRIPURA	11	4,400.64	9,067.42	106.05	7	2,909.18	7,575.96	160.42
24	UTTAR PRADESH	84	1,09,541.15	1,13,231.41	3.37	18	27,633.82	31,778.66	15.00
25	WEST BENGAL	55	56,620.37	71,830.32	26.86	22	25,345.31	40,924.94	61.47
26	D & N HAVELI	1	6,086.08	5,479.75	-9.96	0	0.00	0.00	0.00
27	DELHI	16	50,520.06	50,799.67	0.55	3	1,572.56	1,998.17	27.06
28	CHHATISGARH	38	82,769.79	84,975.67	2.67	5	3,354.55	5,560.43	65.76
29	JHARKHAND	48	46,724.53	50,436.69	7.94	10	9,447.31	13,163.25	39.33
30	UTTARAKHAND	13	16,833.35	17,673.56	4.99	5	5,112.02	8,626.44	68.75
31	ANDAMAN & NICOBAR ISLANDS	1	314.61	441.33	40.28	1	314.61	441.33	40.28
32	TELANGANA	35	24,832.84	27,489.74	10.70	10	3,002.30	5,850.29	94.86
33	MULTI STATE	182	2,99,488.52	2,97,634.29	-0.62	71	68,914.84	1,22,944.12	78.40
Total		1283	15,58,352.33	17,59,443.87	12.90	349	3,37,145.01	6,07,174.02	80.09

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-7

Extent of time overrun in projects with respect to original schedule Rs.150 Crore and above									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost Overrun [^] (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	3	27,271.00	29,779.00	9.20	3	27,271.00	29,779.00	47 - 89
2	CIVIL AVIATION	2	624.07	994.86	59.41	2	624.07	994.86	21 - 81
3	COAL	91	87,760.24	88,310.52	0.63	40	20,946.90	21,229.31	4 - 132
4	FERTILISERS	2	680.64	703.44	3.35	1	197.79	209.44	29 - 29
5	MINES	4	6,773.63	6,773.63	0.00	0	0.00	0.00	-
6	STEEL	32	56,191.76	56,405.44	0.38	15	45,067.07	44,878.86	5 - 72
7	PETROLEUM	109	1,92,892.26	1,94,226.73	0.69	35	60,194.32	63,305.06	1 - 93
8	POWER	126	3,38,804.33	3,97,533.16	17.33	64	2,23,824.94	2,62,161.80	2 - 136
9	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
10	HEALTH AND FAMILY WELFARE	16	4,538.61	4,550.91	0.27	5	1,183.93	1,183.93	6 - 16
11	RAILWAYS	350	3,53,681.04	4,65,297.26	31.56	36	44,219.60	1,22,545.44	12 - 261
12	ROAD TRANSPORT AND HIGHWAYS	495	3,27,076.22	3,33,448.42	1.95	76	62,070.98	65,613.60	5 - 117
13	SHIPPING AND PORTS	8	4,117.75	5,085.02	23.49	2	516.39	1,269.46	96 - 141
14	TELECOMMUNICATIONS	8	16,776.04	28,006.04	66.94	1	13,334.00	24,664.00	47 - 47
15	URBAN DEVELOPMENT	34	1,38,993.10	1,44,033.10	3.63	21	60,252.70	65,438.70	4 - 72
16	DEFENCE PRODUCTION	2	453.64	469.04	3.39	0	0.00	0.00	-
Total		1283	15,58,352.33	17,59,443.87	12.90	302	5,61,421.69	7,07,100.76	

[^] - Cost Overrun = Anticipated Cost minus Original Cost

^{\$} - Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-8
Extent of time overrun in projects with respect to original schedule(State Wise) Rs.150 Crore and above

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost Overrun ^ (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	59	97,031.51	1,01,034.54	4.13	9	10,001.66	11,682.30	10 - 144
2	ARUNACHAL PRADESH	31	16,602.41	33,555.84	102.11	3	3,209.82	7,672.72	36 - 99
3	ASSAM	48	33,455.72	49,152.55	46.92	18	13,573.84	27,890.12	15 - 122
4	BIHAR	78	65,774.22	82,592.48	25.57	9	30,512.63	40,492.75	11 - 98
5	GOA	9	4,043.51	4,058.91	0.38	0	0.00	0.00	-
6	GUJARAT	44	39,186.12	41,822.49	6.73	7	16,203.35	17,884.87	7 - 84
7	HARYANA	21	14,081.22	15,967.45	13.40	2	1,710.95	2,890.95	24 - 76
8	HIMACHAL PRADESH	12	14,659.32	22,591.60	54.11	3	6,107.21	10,586.37	15 - 111
9	JAMMU AND KASHMIR	10	27,408.66	55,639.93	103.00	7	20,944.03	49,175.30	12 - 193
10	KARNATAKA	44	72,280.39	81,988.83	13.43	6	44,544.13	45,244.13	11 - 70
11	KERALA	21	21,774.25	27,871.82	28.00	6	11,313.37	11,420.56	9 - 65
12	MADHYA PRADESH	57	59,615.97	64,062.26	7.46	8	14,436.98	14,919.21	4 - 96
13	MAHARASHTRA	120	1,73,108.23	1,83,029.42	5.73	23	54,553.13	58,822.67	6 - 192
14	MANIPUR	2	944.25	9,874.69	945.77	2	944.25	9,874.69	44 - 108
15	MEGHALAYA	6	7,108.02	9,025.00	26.97	3	1,051.32	1,051.32	15 - 50
16	MIZORAM	5	2,001.20	6,942.57	246.92	2	988.06	5,929.43	71 - 136
17	NAGALAND	7	8,126.79	10,276.79	26.46	4	2,049.11	4,199.11	36 - 60
18	ODISHA	68	72,862.34	80,530.99	10.52	17	26,641.72	27,867.48	3 - 108
19	PUNJAB	28	15,555.77	15,561.50	0.04	4	1,512.09	1,512.09	6 - 23
20	RAJASTHAN	62	44,731.54	47,002.58	5.08	9	17,512.83	18,262.43	6 - 74
21	SIKKIM	6	2,537.08	5,585.45	120.15	2	1,648.94	4,638.22	51 - 81
22	TAMIL NADU	61	67,331.87	82,216.33	22.11	20	38,846.31	47,064.07	1 - 141
23	TRIPURA	11	4,400.64	9,067.42	106.05	3	1,231.33	3,893.38	7 - 72
24	UTTAR PRADESH	84	1,09,541.15	1,13,231.41	3.37	11	24,294.08	24,393.26	3 - 58
25	WEST BENGAL	55	56,620.37	71,830.32	26.86	16	27,379.30	29,531.23	6 - 57
26	D & N HAVELI	1	6,086.08	5,479.75	-9.96	1	6,086.08	5,479.75	5 - 5
27	DELHI	16	50,520.06	50,799.67	0.55	5	3,996.12	4,368.91	5 - 27
28	CHHATISGARH	38	82,769.79	84,975.67	2.67	11	49,049.07	50,029.69	18 - 93
29	JHARKHAND	48	46,724.53	50,436.69	7.94	22	25,136.25	25,488.39	5 - 166
30	UTTARAKHAND	13	16,833.35	17,673.56	4.99	5	7,719.83	11,020.99	50 - 89
31	ANDAMAN & NICOBAR ISLANDS	1	314.61	441.33	40.28	1	314.61	441.33	21 - 21
32	TELANGANA	35	24,832.84	27,489.74	10.70	13	5,449.94	5,987.93	12 - 132
33	MULTI STATE	182	2,99,488.52	2,97,634.29	-0.62	50	92,459.35	1,27,385.11	2 - 261
Total		1283	15,58,352.33	17,59,443.87	12.90	302	5,61,421.69	7,07,100.76	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-9

Extent of time overrun in projects with respect to latest schedule Rs.150 Crore and above									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost Overrun [^] (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	3	29,456.00	29,779.00	1.10	3	29,456.00	29,779.00	47 - 89
2	CIVIL AVIATION	2	624.07	994.86	59.41	2	624.07	994.86	21 - 81
3	COAL	91	88,021.45	88,310.52	0.33	38	14,275.06	14,563.33	0 - 132
4	FERTILISERS	2	692.29	703.44	1.61	0	0.00	0.00	-
5	MINES	4	6,773.63	6,773.63	0.00	0	0.00	0.00	-
6	STEEL	32	56,572.73	56,405.44	-0.30	14	29,566.46	29,353.86	5 - 72
7	PETROLEUM	109	1,95,147.88	1,94,226.73	-0.47	12	11,685.66	12,781.33	1 - 74
8	POWER	126	3,74,261.15	3,97,533.16	6.22	49	2,09,304.18	2,19,632.36	0 - 111
9	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
10	HEALTH AND FAMILY WELFARE	16	4,538.61	4,550.91	0.27	4	819.94	819.94	6 - 16
11	RAILWAYS	350	3,77,157.73	4,65,297.26	23.37	39	64,721.90	1,25,628.41	0 - 261
12	ROAD TRANSPORT AND HIGHWAYS	495	3,27,650.24	3,33,448.42	1.77	76	62,086.75	65,613.60	5 - 117
13	SHIPPING AND PORTS	8	4,131.25	5,085.02	23.09	2	516.39	1,269.46	96 - 141
14	TELECOMMUNICATIONS	8	16,776.04	28,006.04	66.94	1	13,334.00	24,664.00	47 - 47
15	URBAN DEVELOPMENT	34	1,44,813.50	1,44,033.10	-0.54	17	64,852.54	64,217.96	5 - 72
16	DEFENCE PRODUCTION	2	454.00	469.04	3.31	0	0.00	0.00	-
Total		1283	16,28,788.57	17,59,443.87	8.02	258	5,02,960.95	5,93,145.41	

[^] - Cost Overrun = Anticipated Cost minus latest approved cost

\$- Time overrun = Anticipated Date of Commissioning minus latest approved Date of Commissioning

TABLE-10

Extent of cost overrun in projects with respect to latest schedule RS.150 Crore and above									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overruns [^]			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun [^] (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	3	29,456.00	29,779.00	1.10	1	5,677.00	6,000.00	5.69
2	CIVIL AVIATION	2	624.07	994.86	59.41	2	624.07	994.86	59.41
3	COAL	91	88,021.45	88,310.52	0.33	3	17,915.37	18,213.99	1.67
4	FERTILISERS	2	692.29	703.44	1.61	1	482.85	494.00	2.31
5	MINES	4	6,773.63	6,773.63	0.00	0	0.00	0.00	0.00
6	STEEL	32	56,572.73	56,405.44	-0.30	3	1,586.97	1,777.68	12.02
7	PETROLEUM	109	1,95,147.88	1,94,226.73	-0.47	8	12,243.82	15,459.12	26.26
8	POWER	126	3,74,261.15	3,97,533.16	6.22	16	51,034.45	74,306.46	45.60
9	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
10	HEALTH AND FAMILY WELFARE	16	4,538.61	4,550.91	0.27	1	196.70	209.00	6.25
11	RAILWAYS	350	3,77,157.73	4,65,297.26	23.37	200	1,36,891.94	2,83,702.40	107.25
12	ROAD TRANSPORT AND HIGHWAYS	495	3,27,650.24	3,33,448.42	1.77	33	23,181.71	29,854.53	28.78
13	SHIPPING AND PORTS	8	4,131.25	5,085.02	23.09	5	1,219.00	2,172.77	78.24
14	TELECOMMUNICATIONS	8	16,776.04	28,006.04	66.94	1	13,334.00	24,664.00	84.97
15	URBAN DEVELOPMENT	34	1,44,813.50	1,44,033.10	-0.54	2	662.97	666.80	0.58
16	DEFENCE PRODUCTION	2	454.00	469.04	3.31	2	454.00	469.04	3.31
Total		1283	16,28,788.57	17,59,443.87	8.02	279	2,67,222.85	4,62,811.95	73.19

[^] - Cost Overrun = Anticipated Cost minus latest approved Cost

TABLE-11

Extent of time & cost overrun in projects with respect to latest schedule Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	3	29,456.00	29,779.00	1.10	1	5,677.00	6,000.00	89- 89
2	CIVIL AVIATION	2	624.07	994.86	59.41	2	624.07	994.86	21- 81
3	COAL	91	88,021.45	88,310.52	0.33	2	678.37	976.19	72- 132
4	FERTILISERS	2	692.29	703.44	1.61	0	0.00	0.00	0- 0
5	MINES	4	6,773.63	6,773.63	0.00	0	0.00	0.00	0- 0
6	STEEL	32	56,572.73	56,405.44	-0.30	1	343.00	488.40	17- 17
7	PETROLEUM	109	1,95,147.88	1,94,226.73	-0.47	3	2,216.91	3,332.03	20- 70
8	POWER	126	3,74,261.15	3,97,533.16	6.22	10	30,390.49	40,718.67	11- 111
9	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75- 75
10	HEALTH AND FAMILY WELFARE	16	4,538.61	4,550.91	0.27	0	0.00	0.00	0- 0
11	RAILWAYS	350	3,77,157.73	4,65,297.26	23.37	28	45,909.50	1,05,810.14	33- 261
12	ROAD TRANSPORT AND HIGHWAYS	495	3,27,650.24	3,33,448.42	1.77	7	3,665.56	7,192.92	63- 112
13	SHIPPING AND PORTS	8	4,131.25	5,085.02	23.09	2	516.39	1,269.46	96- 141
14	TELECOMMUNICATIONS	8	16,776.04	28,006.04	66.94	1	13,334.00	24,664.00	47- 47
15	URBAN DEVELOPMENT	34	1,44,813.50	1,44,033.10	-0.54	1	166.97	170.62	72- 72
16	DEFENCE PRODUCTION	2	454.00	469.04	3.31	0	0.00	0.00	0- 0
Total		1283	16,28,788.57	17,59,443.87	8.02	59	1,05,240.26	1,95,444.59	

^ - Cost Overrun = Anticipated Cost minus latest approved Cost

\$- Time overrun = Anticipated Date of Commissioning minus latest approved Date of Commissioning

TABLE-12

Extent of time & cost overrun in projects with respect to original schedule Rs.150 Crore and above									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	3	27,271.00	29,779.00	9.20	1	3,492.00	6,000.00	89- 89
2	CIVIL AVIATION	2	624.07	994.86	59.41	2	624.07	994.86	21- 81
3	COAL	91	87,760.24	88,310.52	0.63	6	1,929.87	3,064.27	4- 132
4	FERTILISERS	2	680.64	703.44	3.35	1	197.79	209.44	29- 29
5	MINES	4	6,773.63	6,773.63	0.00	0	0.00	0.00	0- 0
6	STEEL	32	56,191.76	56,405.44	0.38	2	545.61	715.40	12- 17
7	PETROLEUM	109	1,92,892.26	1,94,226.73	0.69	11	19,164.96	24,662.65	9- 70
8	POWER	126	3,38,804.33	3,97,533.16	17.33	36	86,011.39	1,24,348.25	11- 136
9	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75- 75
10	HEALTH AND FAMILY WELFARE	16	4,538.61	4,550.91	0.27	0	0.00	0.00	0- 0
11	RAILWAYS	350	3,53,681.04	4,65,297.26	31.56	29	29,257.73	1,07,592.12	33- 261
12	ROAD TRANSPORT AND HIGHWAYS	495	3,27,076.22	3,33,448.42	1.95	8	3,804.49	7,347.92	36- 112
13	SHIPPING AND PORTS	8	4,117.75	5,085.02	23.49	2	516.39	1,269.46	96- 141
14	TELECOMMUNICATIONS	8	16,776.04	28,006.04	66.94	1	13,334.00	24,664.00	47- 47
15	URBAN DEVELOPMENT	34	1,38,993.10	1,44,033.10	3.63	5	16,524.82	21,745.20	5- 70
16	DEFENCE PRODUCTION	2	453.64	469.04	3.39	0	0.00	0.00	0- 0
Total		1283	15,58,352.33	17,59,443.87	12.90	105	1,77,121.12	3,26,440.87	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

Table-13

State-Wise Position of Central Sector Projects costing Rs. 150 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	59	97,031.51	1,01,034.54	4.13	3	1,241.74	3,280.38	17 - 144
2	ARUNACHAL PRADESH	31	16,602.41	33,555.84	102.11	3	3,209.82	7,672.72	36 - 99
3	ASSAM	48	33,455.72	49,152.55	46.92	10	9,674.41	24,096.40	32 - 122
4	BIHAR	78	65,774.22	82,592.48	25.57	4	27,447.25	37,427.37	11 - 98
5	GOA	9	4,043.51	4,058.91	0.38	0	0.00	0.00	-
6	GUJARAT	44	39,186.12	41,822.49	6.73	2	1,827.34	3,559.49	63 - 84
7	HARYANA	21	14,081.22	15,967.45	13.40	1	1,108.00	2,288.00	76 - 76
8	HIMACHAL PRADESH	12	14,659.32	22,591.60	54.11	1	3,919.59	8,398.75	111 - 111
9	JAMMU AND KASHMIR	10	27,408.66	55,639.93	103.00	3	7,930.45	36,161.72	12 - 193
10	KARNATAKA	44	72,280.39	81,988.83	13.43	1	993.00	1,693.00	70 - 70
11	KERALA	21	21,774.25	27,871.82	28.00	1	607.06	714.25	17 - 17
12	MADHYA PRADESH	57	59,615.97	64,062.26	7.46	2	946.60	1,436.57	72 - 96
13	MAHARASHTRA	120	1,73,108.23	1,83,029.42	5.73	9	15,706.53	21,470.35	12 - 192
14	MANIPUR	2	944.25	9,874.69	945.77	1	727.56	9,658.00	108 - 108
15	MEGHALAYA	6	7,108.02	9,025.00	26.97	0	0.00	0.00	-
16	MIZORAM	5	2,001.20	6,942.57	246.92	2	988.06	5,929.43	71 - 136
17	NAGALAND	7	8,126.79	10,276.79	26.46	1	850.00	3,000.00	60 - 60
18	ODISHA	68	72,862.34	80,530.99	10.52	2	316.64	1,542.70	58 - 105
19	PUNJAB	28	15,555.77	15,561.50	0.04	0	0.00	0.00	-
20	RAJASTHAN	62	44,731.54	47,002.58	5.08	3	1,832.95	2,582.55	33 - 63
21	SIKKIM	6	2,537.08	5,585.45	120.15	2	1,648.94	4,638.22	51 - 81
22	TAMIL NADU	61	67,331.87	82,216.33	22.11	7	23,144.44	32,111.31	4 - 141
23	TRIPURA	11	4,400.64	9,067.42	106.05	2	1,015.95	3,678.00	12 - 72
24	UTTAR PRADESH	84	1,09,541.15	1,13,231.41	3.37	1	195.42	294.60	58 - 58
25	WEST BENGAL	55	56,620.37	71,830.32	26.86	3	11,432.55	13,584.49	9 - 57
26	D & N HAVELI	1	6,086.08	5,479.75	-9.96	0	0.00	0.00	-
27	DELHI	16	50,520.06	50,799.67	0.55	1	1,219.21	1,592.00	5 - 5
28	CHHATISGARH	38	82,769.79	84,975.67	2.67	3	2,223.98	3,204.60	40 - 93
29	JHARKHAND	48	46,724.53	50,436.69	7.94	2	1,161.75	1,513.89	99 - 166
30	UTTARAKHAND	13	16,833.35	17,673.56	4.99	3	4,749.74	8,051.41	58 - 84
31	ANDAMAN & NICOBAR ISLANDS	1	314.61	441.33	40.28	1	314.61	441.33	21 - 21
32	TELANGANA	35	24,832.84	27,489.74	10.70	4	1,463.44	2,104.31	33 - 132
33	MULTI STATE	182	2,99,488.52	2,97,634.29	-0.62	27	49,224.09	84,315.03	13 - 261
Total		1283	15,58,352.33	17,59,443.87	12.90	105	1,77,121.12	3,26,440.87	

TABLE-14

EXECUTIVE SUMMARY COSTING Rs.1000 crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	131	3
2	ROAD TRANSPORT AND HIGHWAYS	105	1
3	POWER	65	14
4	PETROLEUM	42	2
5	COAL	12	1
6	URBAN DEVELOPMENT	10	0
7	STEEL	9	2
8	ATOMIC ENERGY	3	1
9	TELECOMMUNICATIONS	2	1
10	MINES	1	0
11	HEAVY INDUSTRY	1	0
12	SHIPPING AND PORTS	1	0
	Total	382	25

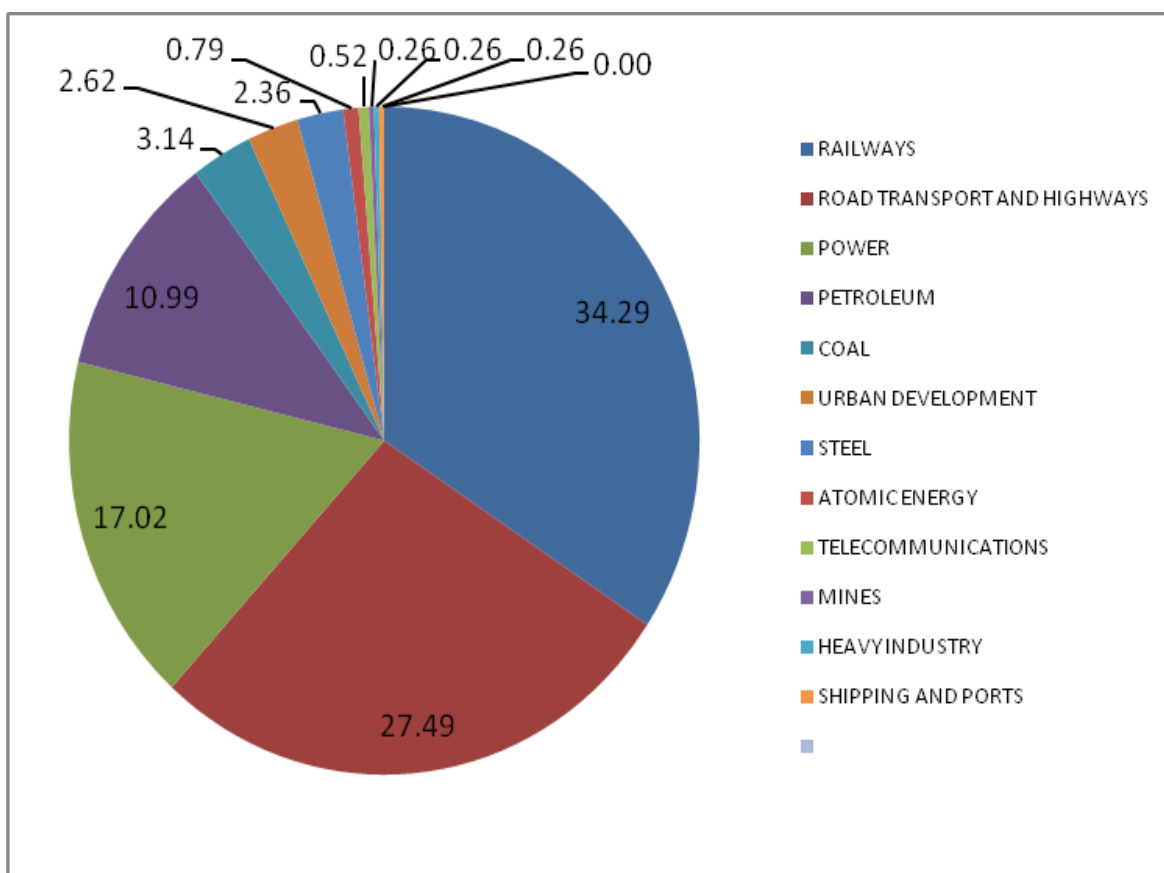


TABLE-15

Projects Added / Completed / Dropped / Frozen Rs.1000 Crore and above

No of Projects in Previous Month	380
No of Projects Completed/Dropped/Frozen in Current Month	4
No of Projects added in Current Month	4
No of Projects upgraded to the status of Mega Projects	2
No of Projects in Current Month	382

Project status Rs. 1000 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	129 (33.77%)	4 (1.05%)	87 (22.77%)	48 (12.57%)	114 (29.84%)	382
Latest Approved (Date)	105 (27.49%)	3 (.79%)	114 (29.84%)	45 (11.78%)	115 (30.10%)	382

Project cost Rs.1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	323	10,32,458.96	11,20,003.78	3,88,454.90	34.70	87,544.82	8.50
Project with Revision in Cost	59	2,26,804.33	2,44,580.61	1,55,752.02	63.70	17,776.28	7.80
Total	382	12,59,263.29	13,64,584.39	5,44,206.92	39.88	1,05,321.10	8.36
Original Cost of All Projects							
Original Cost	382	11,92,573.37	13,64,584.39	5,44,206.92	39.88	1,72,011.02	14.42

Delayed Project cost Rs.1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	129	4,93,746.71	6,32,566.27	3,84,278.65	60.70	1,38,819.56	28.10
Latest Approved (RCE)	105	4,41,337.60	5,26,789.83	3,03,688.99	57.60	85,452.23	19.40
Additional Delayed Project cost Rs.1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	25	1,66,035.26	1,89,385.68	1,23,475.40	65.20	23,350.42	14.10

TABLE-16

Extent of cost overrun in projects with respect to original schedule(Sector Wise) Rs.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	3	27,271.00	29,779.00	9.20	1	3,492.00	6,000.00	71.82
2	COAL	12	55,807.73	55,808.53	0.00	1	17,237.00	17,237.80	0.00
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
4	STEEL	9	48,164.22	48,150.68	-0.03	1	768.88	1,113.34	44.80
5	PETROLEUM	42	1,65,237.15	1,66,989.32	1.06	9	21,796.28	27,032.81	24.02
6	POWER	65	3,14,747.99	3,71,924.17	18.17	27	97,751.62	1,54,927.80	58.49
7	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
8	RAILWAYS	131	2,71,311.16	3,58,438.42	32.11	86	83,897.49	2,30,244.38	174.44
9	ROAD TRANSPORT AND HIGHWAYS	105	1,52,134.41	1,57,570.47	3.57	15	17,413.21	22,849.27	31.22
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0.00
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	84.97
12	URBAN DEVELOPMENT	10	1,32,769.14	1,37,453.93	3.53	2	15,819.21	20,650.00	30.54
Total		382	11,92,573.37	13,64,584.39	14.42	144	2,73,227.69	5,08,546.70	86.13

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-17

Extent of cost overrun in projects with respect to original schedule (State Wise) Rs.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun [^]			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	16	82,287.82	84,885.89	3.16	4	5,360.88	8,685.95	62.02
2	ARUNACHAL PRADESH	4	10,609.32	27,330.31	157.61	3	9,356.22	26,077.21	178.72
3	ASSAM	9	21,033.85	34,843.26	65.65	5	12,723.01	26,619.00	109.22
4	BIHAR	13	37,034.94	51,767.80	39.78	7	28,983.86	43,716.72	50.83
5	GUJARAT	10	23,570.79	26,172.48	11.04	3	3,221.99	5,823.68	80.75
6	HARYANA	4	5,634.39	6,814.39	20.94	1	1,108.00	2,288.00	106.50
7	HIMACHAL PRADESH	6	12,226.08	20,158.36	64.88	2	4,966.47	12,898.75	159.72
8	JAMMU AND KASHMIR	10	27,408.66	55,639.93	103.00	3	7,930.45	36,161.72	355.99
9	KARNATAKA	20	60,672.06	69,275.41	14.18	11	7,389.10	16,751.45	126.70
10	KERALA	7	16,657.19	22,154.71	33.00	2	1,450.00	6,947.52	379.14
11	MADHYA PRADESH	15	38,561.17	42,526.03	10.28	6	5,173.40	9,138.26	76.64
12	MAHARASHTRA	44	1,42,261.61	1,50,501.32	5.79	17	29,763.57	41,277.58	38.68
13	MANIPUR	1	727.56	9,658.00	1227.45	1	727.56	9,658.00	1227.45
14	MEGHALAYA	2	5,577.50	7,494.48	34.37	1	4,083.02	6,000.00	46.95
15	MIZORAM	2	988.06	5,929.43	500.11	2	988.06	5,929.43	500.11
16	NAGALAND	3	6,420.00	8,570.00	33.49	1	850.00	3,000.00	252.94
17	ODISHA	24	56,413.98	63,001.36	11.68	6	3,733.20	10,320.58	176.45
18	PUNJAB	2	2,557.95	2,557.95	0.00	0	0.00	0.00	0.00
19	RAJASTHAN	7	19,624.78	19,956.68	1.69	1	829.74	1,161.64	40.00
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	204.95
21	TAMIL NADU	17	48,607.00	61,638.69	26.81	8	23,853.78	36,885.47	54.63
22	TRIPURA	3	2,129.35	6,386.31	199.92	3	2,129.35	6,386.31	199.92
23	UTTAR PRADESH	33	86,307.66	88,855.18	2.95	7	23,509.18	26,511.28	12.77
24	WEST BENGAL	22	44,076.95	56,813.51	28.90	10	22,275.61	35,012.18	57.18
25	D & N HAVELI	1	6,086.08	5,479.75	-9.96	0	0.00	0.00	0.00
26	DELHI	4	45,462.73	45,689.52	0.50	1	1,219.21	1,592.00	30.58
27	CHHATISGARH	11	71,673.86	73,381.18	2.38	3	2,877.22	4,584.54	59.34
28	JHARKHAND	10	33,188.25	35,781.77	7.81	3	7,451.01	10,044.53	34.81
29	UTTARAKHAND	6	14,392.36	14,868.59	3.31	2	4,635.48	7,785.41	67.95
30	TELANGANA	6	14,904.53	16,572.01	11.19	2	502.99	2,170.47	331.51
31	MULTI STATE	69	2,54,137.41	2,45,795.40	-3.28	28	54,795.85	1,01,034.33	84.38
Total		382	11,92,573.37	13,64,584.39	14.42	144	2,73,227.69	5,08,546.70	86.13

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-18

Extent of time overrun in projects with respect to original schedule Rs.1000 Crore and above

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	3	27,271.00	29,779.00	9.20	3	27,271.00	29,779.00	47 - 89
2	COAL	12	55,807.73	55,808.53	0.00	3	8,192.43	8,192.43	24 - 48
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	-
4	STEEL	9	48,164.22	48,150.68	-0.03	6	40,963.49	40,605.49	5 - 57
5	PETROLEUM	42	1,65,237.15	1,66,989.32	1.06	17	52,938.39	55,548.93	5 - 74
6	POWER	65	3,14,747.99	3,71,924.17	18.17	42	2,13,950.34	2,50,806.80	2 - 136
7	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
8	RAILWAYS	131	2,71,311.16	3,58,438.42	32.11	25	39,634.09	1,15,657.79	12 - 261
9	ROAD TRANSPORT AND HIGHWAYS	105	1,52,134.41	1,57,570.47	3.57	26	39,658.83	42,567.60	15 - 76
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	-
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	47 - 47
12	URBAN DEVELOPMENT	10	1,32,769.14	1,37,453.93	3.53	5	56,086.14	60,916.93	5 - 29
Total		382	11,92,573.37	13,64,584.39	14.42	129	4,93,746.71	6,32,566.27	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-20

Extent of time overrun in projects with respect to latest schedule Rs.1000 Crore and above									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost Overrun [^] (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	3	29,456.00	29,779.00	1.10	3	29,456.00	29,779.00	47 - 89
2	COAL	12	55,807.73	55,808.53	0.00	2	2,285.32	2,285.32	24 - 48
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	-
4	STEEL	9	48,466.31	48,150.68	-0.65	5	25,438.49	25,080.49	5 - 57
5	PETROLEUM	42	1,67,666.77	1,66,989.32	-0.40	4	7,889.71	8,918.36	25 - 74
6	POWER	65	3,48,998.34	3,71,924.17	6.57	31	2,00,525.91	2,10,588.07	0 - 111
7	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
8	RAILWAYS	131	2,93,365.00	3,58,438.42	22.18	27	59,476.18	1,18,162.76	0 - 261
9	ROAD TRANSPORT AND HIGHWAYS	105	1,52,134.41	1,57,570.47	3.57	26	39,658.83	42,567.60	15 - 76
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	-
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	47 - 47
12	URBAN DEVELOPMENT	10	1,38,238.16	1,37,453.93	-0.57	5	61,555.16	60,916.93	5 - 29
Total		382	12,59,263.29	13,64,584.39	8.36	105	4,41,337.60	5,26,789.83	

[^] - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-21

Extent of cost overrun in projects with respect to latest schedule RS.1000 Crore and above									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overruns			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	3	29,456.00	29,779.00	1.10	1	5,677.00	6,000.00	5.69
2	COAL	12	55,807.73	55,808.53	0.00	1	17,237.00	17,237.80	0.00
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
4	STEEL	9	48,466.31	48,150.68	-0.65	1	1,070.97	1,113.34	3.96
5	PETROLEUM	42	1,67,666.77	1,66,989.32	-0.40	5	11,374.26	14,442.84	26.98
6	POWER	65	3,48,998.34	3,71,924.17	6.57	10	48,638.02	71,563.85	47.14
7	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
8	RAILWAYS	131	2,93,365.00	3,58,438.42	22.18	80	1,00,175.83	2,22,024.86	121.64
9	ROAD TRANSPORT AND HIGHWAYS	105	1,52,134.41	1,57,570.47	3.57	15	17,413.21	22,849.27	31.22
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0.00
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	84.97
12	URBAN DEVELOPMENT	10	1,38,238.16	1,37,453.93	-0.57	0	0.00	0.00	0.00
Total		382	12,59,263.29	13,64,584.39	8.36	115	2,16,638.29	3,83,723.26	77.13

^ - Cost Overrun = Anticipated Cost minus latest approved Cost

TABLE-21

Extent of time & cost overrun in projects with respect to latest schedule Rs. 1000 Crore and above									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	3	29,456.00	29,779.00	1.10	1	5,677.00	6,000.00	89- 89
2	COAL	12	55,807.73	55,808.53	0.00	0	0.00	0.00	0- 0
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
4	STEEL	9	48,466.31	48,150.68	-0.65	0	0.00	0.00	0- 0
5	PETROLEUM	42	1,67,666.77	1,66,989.32	-0.40	2	1,864.35	2,893.00	32- 70
6	POWER	65	3,48,998.34	3,71,924.17	6.57	7	29,432.98	39,495.14	11- 111
7	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75- 75
8	RAILWAYS	131	2,93,365.00	3,58,438.42	22.18	19	42,164.49	99,836.66	34- 261
9	ROAD TRANSPORT AND HIGHWAYS	105	1,52,134.41	1,57,570.47	3.57	2	2,617.10	5,525.87	63- 76
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0- 0
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	47- 47
12	URBAN DEVELOPMENT	10	1,38,238.16	1,37,453.93	-0.57	0	0.00	0.00	0- 0
Total		382	12,59,263.29	13,64,584.39	8.36	33	96,807.92	1,82,241.97	

^ - Cost Overrun = Anticipated Cost minus latest approved Cost

\$- Time overrun = Anticipated Date of Commissioning minus latest approved Date of Commissioning

TABLE-22

Extent of time & cost overrun in projects with respect to original schedule Rs. 1000 sCrore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	3	27,271.00	29,779.00	9.20	1	3,492.00	6,000.00	89- 89
2	COAL	12	55,807.73	55,808.53	0.00	0	0.00	0.00	0- 0
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
4	STEEL	9	48,164.22	48,150.68	-0.03	0	0.00	0.00	0- 0
5	PETROLEUM	42	1,65,237.15	1,66,989.32	1.06	7	17,692.59	22,455.62	9- 70
6	POWER	65	3,14,747.99	3,71,924.17	18.17	22	80,372.32	1,17,228.78	11- 136
7	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75- 75
8	RAILWAYS	131	2,71,311.16	3,58,438.42	32.11	20	25,594.93	1,01,618.64	34- 261
9	ROAD TRANSPORT AND HIGHWAYS	105	1,52,134.41	1,57,570.47	3.57	2	2,617.10	5,525.87	63- 76
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0- 0
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	47- 47
12	URBAN DEVELOPMENT	10	1,32,769.14	1,37,453.93	3.53	2	15,819.21	20,650.00	5- 24
Total		382	11,92,573.37	13,64,584.39	14.42	56	1,60,640.15	3,01,970.21	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-23

State-Wise Position of Central Sector Projects costing Rs. 1000 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost Overrun [^] (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	16	82,287.82	84,885.89	3.16	1	743.00	1,825.00	144 - 144
2	ARUNACHAL PRADESH	4	10,609.32	27,330.31	157.61	2	3,070.89	7,517.72	55 - 99
3	ASSAM	9	21,033.85	34,843.26	65.65	4	8,423.01	22,099.00	32 - 122
4	BIHAR	13	37,034.94	51,767.80	39.78	3	27,010.57	36,824.93	11 - 98
5	GUJARAT	10	23,570.79	26,172.48	11.04	1	1,509.10	3,237.87	63 - 63
6	HARYANA	4	5,634.39	6,814.39	20.94	1	1,108.00	2,288.00	76 - 76
7	HIMACHAL PRADESH	6	12,226.08	20,158.36	64.88	1	3,919.59	8,398.75	111 - 111
8	JAMMU AND KASHMIR	10	27,408.66	55,639.93	103.00	3	7,930.45	36,161.72	12 - 193
9	KARNATAKA	20	60,672.06	69,275.41	14.18	1	993.00	1,693.00	70 - 70
10	KERALA	7	16,657.19	22,154.71	33.00	0	0.00	0.00	-
11	MADHYA PRADESH	15	38,561.17	42,526.03	10.28	0	0.00	0.00	-
12	MAHARASHTRA	44	1,42,261.61	1,50,501.32	5.79	5	14,423.33	19,503.64	12 - 192
13	MANIPUR	1	727.56	9,658.00	1,227.45	1	727.56	9,658.00	108 - 108
14	MEGHALAYA	2	5,577.50	7,494.48	34.37	0	0.00	0.00	-
15	MIZORAM	2	988.06	5,929.43	500.11	2	988.06	5,929.43	71 - 136
16	NAGALAND	3	6,420.00	8,570.00	33.49	1	850.00	3,000.00	60 - 60
17	ODISHA	24	56,413.98	63,001.36	11.68	1	183.23	1,202.70	58 - 58
18	PUNJAB	2	2,557.95	2,557.95	0.00	0	0.00	0.00	-
19	RAJASTHAN	7	19,624.78	19,956.68	1.69	1	829.74	1,161.64	57 - 57
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	51 - 51
21	TAMIL NADU	17	48,607.00	61,638.69	26.81	4	21,811.42	29,947.97	24 - 118
22	TRIPURA	3	2,129.35	6,386.31	199.92	1	813.34	3,451.00	72 - 72
23	UTTAR PRADESH	33	86,307.66	88,855.18	2.95	0	0.00	0.00	-
24	WEST BENGAL	22	44,076.95	56,813.51	28.90	3	11,432.55	13,584.49	9 - 57
25	D & N HAVELI	1	6,086.08	5,479.75	-9.96	0	0.00	0.00	-
26	DELHI	4	45,462.73	45,689.52	0.50	1	1,219.21	1,592.00	5 - 5
27	CHHATISGARH	11	71,673.86	73,381.18	2.38	1	1,746.65	2,228.71	40 - 40
28	JHARKHAND	10	33,188.25	35,781.77	7.81	1	900.05	1,125.89	99 - 99
29	UTTARAKHAND	6	14,392.36	14,868.59	3.31	2	4,635.48	7,785.41	58 - 84
30	TELANGANA	6	14,904.53	16,572.01	11.19	0	0.00	0.00	-
31	MULTI STATE	69	2,54,137.41	2,45,795.40	-3.28	14	44,032.44	77,668.65	20 - 261
Total		382	11,92,573.37	13,64,584.39	14.42	56	1,60,640.15	3,01,970.21	

[^] - Cost Overrun = Anticipated Cost minus Original Cost

^{\$} - Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-24

List of projects completed/dropped/Frozen during current month Rs.150 Crore and above (All Cost/ Expenditure in Rs. crore)							
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>COAL</u>						
1	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU	04/2012	364.75	10/2014	364.75	10/2017	333.05
	<u>PETROLEUM</u>						
2	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY	02/2014	163.88	07/2016	163.88	10/2017	82.45
3	50 MW 10 PERSENT WIND ENERGY POWER PROJECT Central Sector Projects	11/2015	500.00	03/2017	435.00	10/2017	368.24
4	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT)	06/2012	150.00	07/2014	259.93	10/2017	251.90
	<u>POWER</u>						
5	TRANSMISSION SYSTEM ASSOCIATED WITH IPPTS OF NAGAPATTINAM CUDDALORE AREA – PACKAGE A Central Sector Projects	03/2015	955.00	12/2015	1,364.00	03/2018	74.00
6	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-A Central Sector Projects	04/2015	2,525.00	11/2017	2,525.00	11/2017	564.00
	<u>RAILWAYS</u>						
7	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR	02/1997	295.00	N.A.	1,289.92	10/2017	1,509.88
8	GURIYA-MARWAR AND KARJODA-PALANPUR	04/2011	239.73	N.A.	257.78	10/2017	195.42
9	HOSADURGA - CHICKJAJUR (28.89 KM)	04/2010	203.40	N.A.	273.84	10/2017	282.69
	<u>STEEL</u>						
10	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS	07/2011	877.73	07/2015	877.73	10/2017	747.81

List of projects completed/dropped/Frozen during current month Rs.150 Crore and above
(All Cost/ Expenditure in Rs. crore)

			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
11	TURBO BLOWER - 5 G	12/2009	280.00	09/2016	280.00	10/2017	157.09
	<u>URBAN DEVELOPMENT</u>						
12	BANGALORE METRO RAIL PROJECT G	05/2006	6,395.00	06/2011	13,845.01	10/2017	14,200.11
13	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA G	12/2012	315.00	06/2015	315.00	10/2017	302.82
14	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI G	05/2012	405.01	12/2014	405.01	10/2017	349.54

TABLE-25

List of projects added Rs. 150 Crore and above					(October 2017)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>HEALTH AND FAMILY WELFARE</u>					
1	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA Central Sector Projects	8/2017	274.19	3/2019	274.19	3/2019
2	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH Central Sector Projects	8/2017	272.19	3/2019	272.19	3/2019
3	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL Central Sector Projects	8/2017	355.15	3/2019	355.15	3/2019
	<u>PETROLEUM</u>					
4	AUGMENTATION OF CTMPL Central Sector Projects	12/2016	228.00	6/2020	228.00	6/2020
5	REPLACEMENT OF KV SECTION OF KSPL Central Sector Projects	10/2014	279.00	8/2018	279.00	8/2017
6	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI Central Sector Projects	4/2017	287.49	4/2022	287.49	4/2022
7	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR Central Sector Projects	7/2017	268.79	7/2022	268.79	7/2022
8	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY Central Sector Projects	1/2017	474.15	5/2019	474.15	5/2019
9	DEVELOPMENT OF B-147 FIELD Central Sector Projects	2/2017	546.15	11/2019	546.15	11/2019
10	DEVELOPMENT OF BSE-11 BLOCK Central Sector Projects	2/2017	511.30	11/2019	511.30	11/2019
11	4TH PHASE DEVELOPMENT OF NBP FIELD Central Sector Projects	2/2017	968.61	11/2019	968.61	11/2019
	<u>POWER</u>					
12	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT Central Sector Projects	5/2017	175.64	9/2018	175.64	9/2018
13	HVDC BIPOLE LINK BETWEEN WR AND SR - NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN Central Sector Projects	8/2017	1,931.39	2/2020	1,931.39	2/2020
14	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY Central Sector Projects	5/2017	186.17	7/2019	186.17	7/2019

List of projects added Rs. 150 Crore and above					(October 2017)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
15	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) Central Sector Projects	5/2017	445.89	2/2019	445.89	2/2019
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
16	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 Central Sector Projects	8/2017	950.64	8/2017	950.64	8/2017
17	FOUR LANNING OF CHOLOPURAM-THANJAVUR Central Sector Projects	8/2017	1,176.37	8/2017	1,176.37	8/2017
18	TWO LANE WITH PS OF KARAUKUDI-RAMANATHPURAM Central Sector Projects	8/2017	652.55	8/2017	652.55	8/2017
19	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) Central Sector Projects	6/2017	648.33	6/2017	648.33	6/2017
20	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. Central Sector Projects	10/2017	639.97	10/2017	639.97	10/2017
21	4-LANNING OF STHIYATHOPU-CHOLOPURAM Central Sector Projects	9/2017	1,227.87	9/2017	1,227.87	9/2017
22	4-LANNING OF OTTANCHATRAM BYPASS Central Sector Projects	9/2017	244.27	9/2017	244.27	9/2017
23	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 Central Sector Projects	9/2017	990.61	9/2017	990.61	9/2017
24	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 Central Sector Projects	9/2017	374.40	9/2017	374.40	9/2017
25	4-LANNING OF THALSERRY -MAHE BYPASS Central Sector Projects	9/2017	1,124.11	9/2017	1,124.11	9/2017
26	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 Central Sector Projects	10/2017	964.17	10/2017	964.17	10/2017
27	JUNAGADH BYPASS Central Sector Projects	10/2017	232.49	10/2017	232.49	10/2017
28	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) Central Sector Projects	7/2017	476.56	7/2017	476.56	7/2017
	<u>TELECOMMUNICATIONS</u>					
29	MAHARASHTRA NODAL (LOT 1) Central Sector Projects	8/2017	156.00	4/2018	156.00	4/2018
30	MAHARASHTRA CORE (LOT1) Central Sector Projects	8/2017	156.77	4/2018	156.77	4/2018
31	MAHARASHTRA ACESS (LOT 1)	8/2017	213.00	5/2018	213.00	5/2018

List of projects added Rs. 150 Crore and above					(October 2017)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	Central Sector Projects					
32	MADHYA PRADESH ACCESS (LOT1) Central Sector Projects	8/2017	215.30	5/2018	215.30	5/2018
33	GUJARAT ACCESS (LOT 1) Central Sector Projects	9/2017	171.54	4/2018	171.54	4/2018
	<u>URBAN DEVELOPMENT</u>					
34	NSG AT KOLKATA Central Sector Projects	10/2014	162.88	4/2018	162.88	6/2019

TABLE-26

Milestones (Cumulative due & achieved) Rs. 150 Crore and above

Total	3883
Achieved up to month	2000


TABLE-27

<u>List of projects reporting additional delayed</u> Rs. 150 Crore and above							(October 2017)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>ATOMIC ENERGY</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) BHAVNI G	3,492.00	6,000.00	09/2010	10/2017	02/2018	4
	<u>CIVIL AVIATION</u>						
2	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT AAI G	309.46	553.53	01/2011	09/2017	10/2017	1
	<u>COAL</u>						
3	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) WCL G	328.00	328.00	03/2021	03/2021	06/2022	15
4	SONEPUR BAZARI (COMB) OCP (8.0 MTY) ECL G	1,055.05	1,055.05	03/2018	09/2018	03/2020	18
	<u>STEEL</u>						
5	REBUILDING OF COB-7 AT BSL SAIL G	245.67	245.67	05/2016	10/2017	11/2017	1
6	3RD CONVERTER AND 4TH CASTER RINL G	974.76	974.76	07/2016	10/2017	11/2017	1
7	EXPANSION OF BHILAI STEEL PLANT SAIL G	17,265.00	17,265.00	03/2013	10/2017	12/2017	2
8	COKE OVEN BATTERY-5 RINL G	2,858.00	2,500.00	12/2017	06/2018	10/2018	4
	<u>PETROLEUM</u>						
9	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR ISPRL G	993.00	1,693.00	01/2012	10/2017	11/2017	1
10	DHDS REVAMP FOR MEETING BS-IV DIESEL QUALITY Central Sector Projects CPCL	367.11	367.11	04/2017	11/2017	12/2017	1
11	RESID UPGRADATION PROJECT CPCL G	3,110.36	3,110.36	11/2015	10/2017	12/2017	2
	<u>POWER</u>						
12	KUDGI STPP STAGE 1 NTPC G	15,166.19	15,166.19	01/2017	11/2017	12/2017	1
13	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) CVPPPL G	8,112.12	8,112.12	04/2020	05/2023	06/2023	1


<u>List of projects reporting additional delayed</u> Rs. 150 Crore and above							(October 2017)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
14	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) PGCIL G	305.04	305.04	03/2017	11/2017	12/2017	1
15	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A) PGCIL Central Sector Projects	2,525.00	2,525.00	11/2017	11/2017	01/2018	2
16	BONGAIGAON THERMAL POWER PROJECT NTPC G	4,375.35	8,149.00	09/2011	12/2017	03/2018	3
17	SYSTEM STRENGTHENING XIII OF SR GRID PGCIL G	487.49	639.46	06/2014	06/2018	09/2018	3
18	TANDA TPP STAGE-II (2X660 MW) NTPC G	9,188.98	9,188.98	03/2019	03/2019	06/2019	3
19	DARLIPALLI STPP STAGE-I (2X800 MW) NTPC G	12,532.44	12,532.44	08/2018	08/2018	11/2018	3
20	NPGCPL-NABINAGAR STPP - JV (3X660 MW) NTPC Joint Venture	12,964.60	13,731.26	01/2018	08/2018	12/2018	4
21	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I NTPC G	11,638.55	11,638.55	09/2017	03/2018	09/2018	6
22	SOLAPUR STPP NTPC G	9,395.18	9,395.18	11/2016	04/2018	12/2018	8
23	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) NTPC G	11,846.00	11,846.00	06/2017	04/2018	12/2018	8
24	BRBCL-NABINAGAR TPP- JV (4X250 MW) NTPC G	5,353.00	7,998.00	05/2014	06/2018	02/2019	8
25	MUNPL-MEJA TPP - JV (2X660 MW) NTPC Joint Venture	9,750.89	9,750.89	12/2016	06/2018	02/2019	8
26	TAPOVAN-VISHNUGAD HEP (4X130MW) NTPC G	2,978.48	3,846.30	03/2013	06/2019	03/2020	9
27	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII PGCIL G	203.28	260.03	07/2017	12/2017	12/2018	12
28	RAMMAM-III HEPP (3X40 MW) NTPC G	1,381.84	1,381.84	09/2019	09/2019	03/2021	18
	<u>HEALTH AND FAMILY WELFARE</u>						
29	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR HSCC G	168.90	168.90	05/2017	12/2017	03/2018	3
30	AIIMS - MOTHER AND CHILD BLOCK HSCC G	204.44	204.44	05/2017	12/2017	06/2018	6
31	AIIMS - OPD(NEW) HSCC G	293.65	293.65	05/2017	12/2017	09/2018	9
	<u>RAILWAYS</u>						

<u>List of projects reporting additional delayed</u> Rs. 150 Crore and above							(October 2017)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
32	BHOJIPUR TANAKPUR VIA PILIBHIT NER G	195.64	474.30	N.A.	10/2017	03/2018	5
33	TALCHER-BIMALAGARH(NL)(ECOR) ECOR G	810.78	1,928.07	N.A.	06/2022	12/2022	6
34	KOTTAVALSA - KORAPUT DOUBLING ECOR G	2,499.71	2,499.71	03/2021	03/2021	03/2022	12
35	KORAPUT - SINGAPUR ROAD DOUBLING ECOR G	2,361.74	2,361.74	03/2021	03/2021	03/2022	12
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
36	NALBARI TO BIJNI (AS-6) NHAI G	225.00	225.00	06/2008	09/2017	10/2017	1
37	SONAPUR TO GUWAHTI (AS-3) NHAI G	245.00	245.00	03/2008	05/2017	11/2017	6
38	SIX LANING OF CHANDIKHOL-JAGATPUR- BHUBANESWAR NHAI PPP (BOT)	1,047.00	1,047.00	06/2014	06/2017	12/2017	6
39	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 NHAI G	200.00	200.00	04/2009	05/2017	12/2017	7
40	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) NHAI G	160.00	160.00	05/2008	05/2017	02/2018	9
	<u>TELECOMMUNICATIONS</u>						
41	NETWORK FOR SPECTRUM DOT G	13,334.00	24,664.00	07/2015	09/2017	06/2019	21
	<u>URBAN DEVELOPMENT</u>						
42	CONSTRUCTION OF 1003 NOS 900 NOS TYPE 2 AND 54 NOS TYPE3 AND 33 NOS TYPE 4 AND 16 NOS TYPE 5 FAMILY CPWD EPC	164.00	164.00	01/2018	03/2018	05/2018	2

Graphical Presentation of All Projects w.r.t. Original Schedule

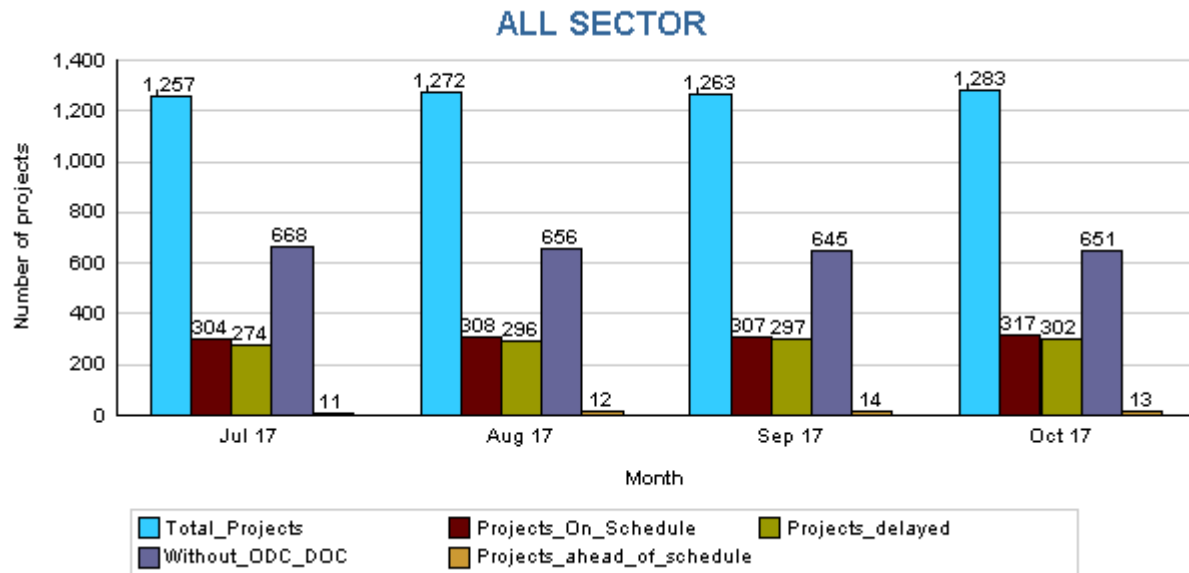


Break-up of 302 Delayed projects in October 2017

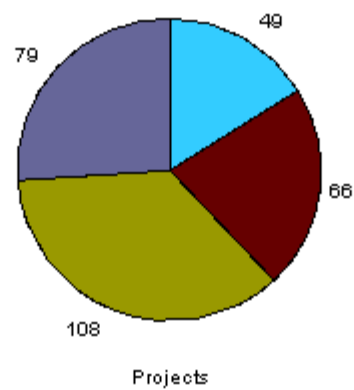


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

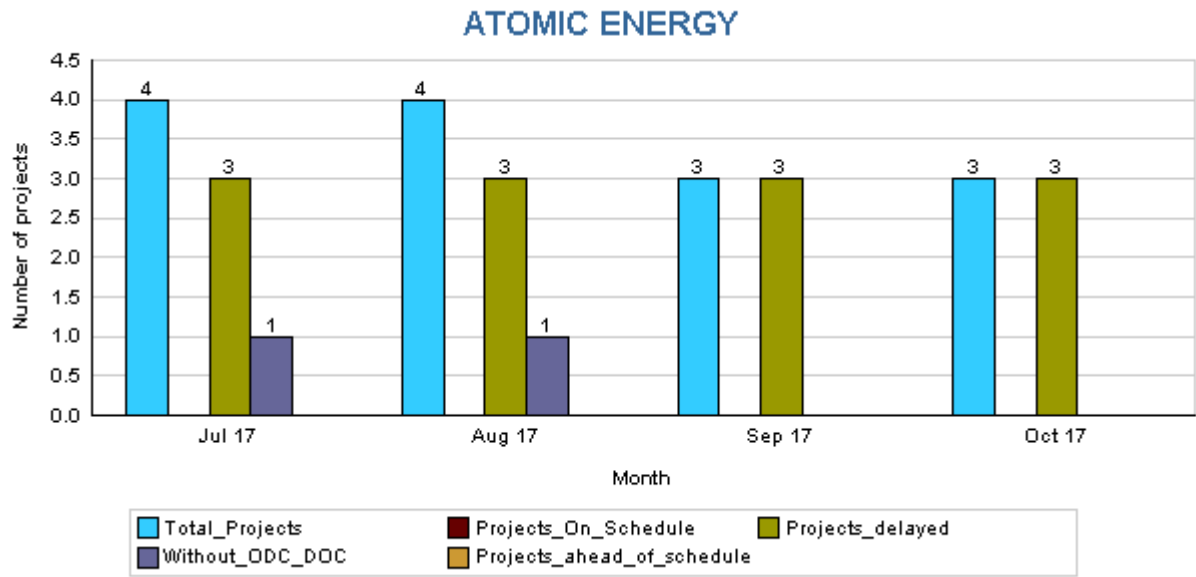


Break-up of 3 Delayed projects in October 2017

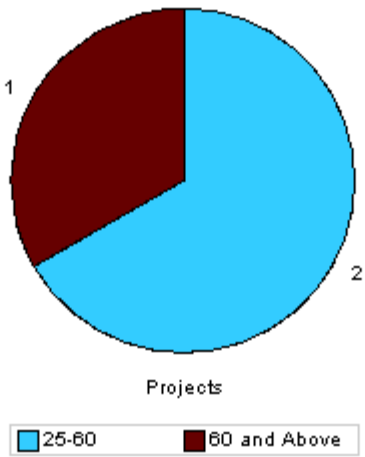


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

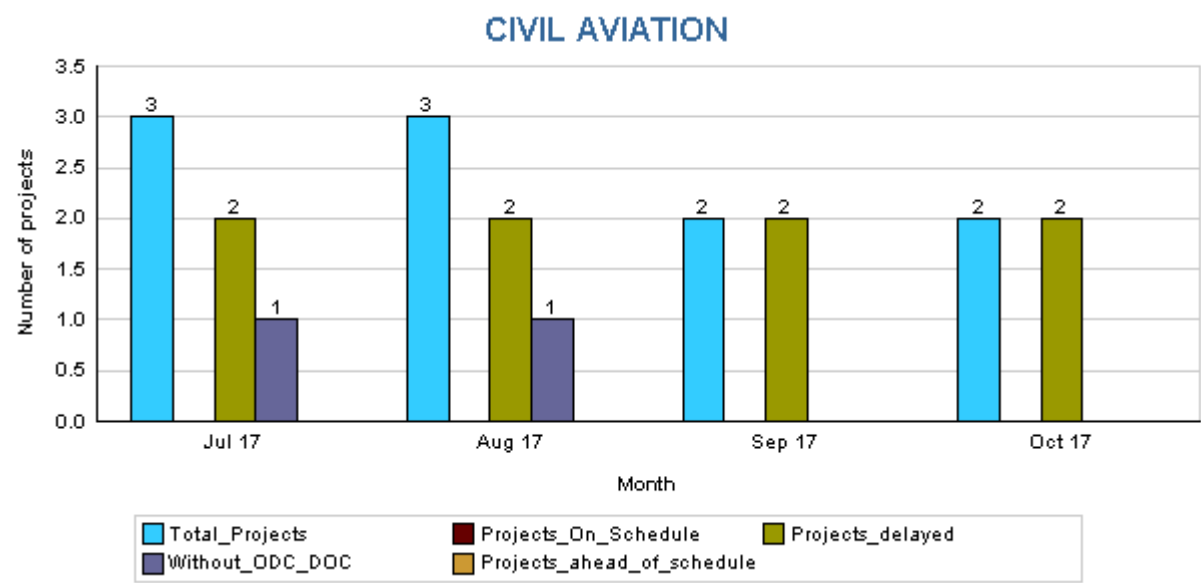


Break-up of 2 Delayed projects in October 2017

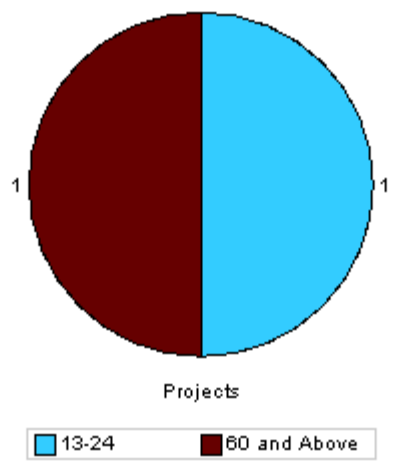


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

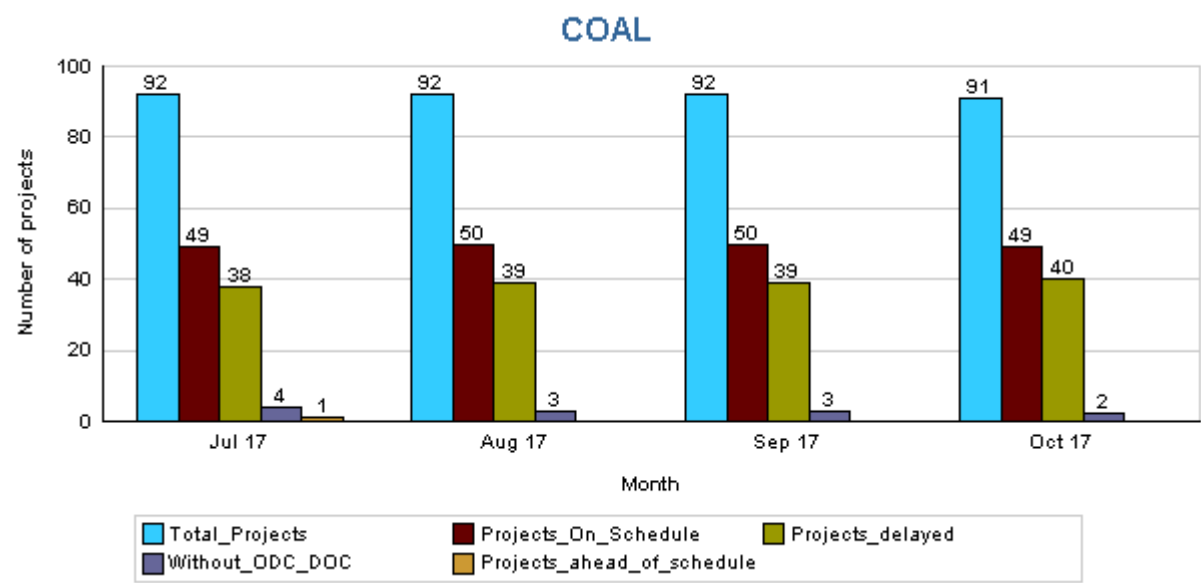


Break-up of 40 Delayed projects in October 2017

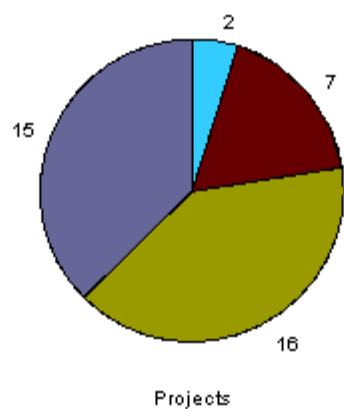


Delay in Months

1-12	13-24	25-60	60 and Above


Graphical Presentation of All Projects w.r.t. Original Schedule

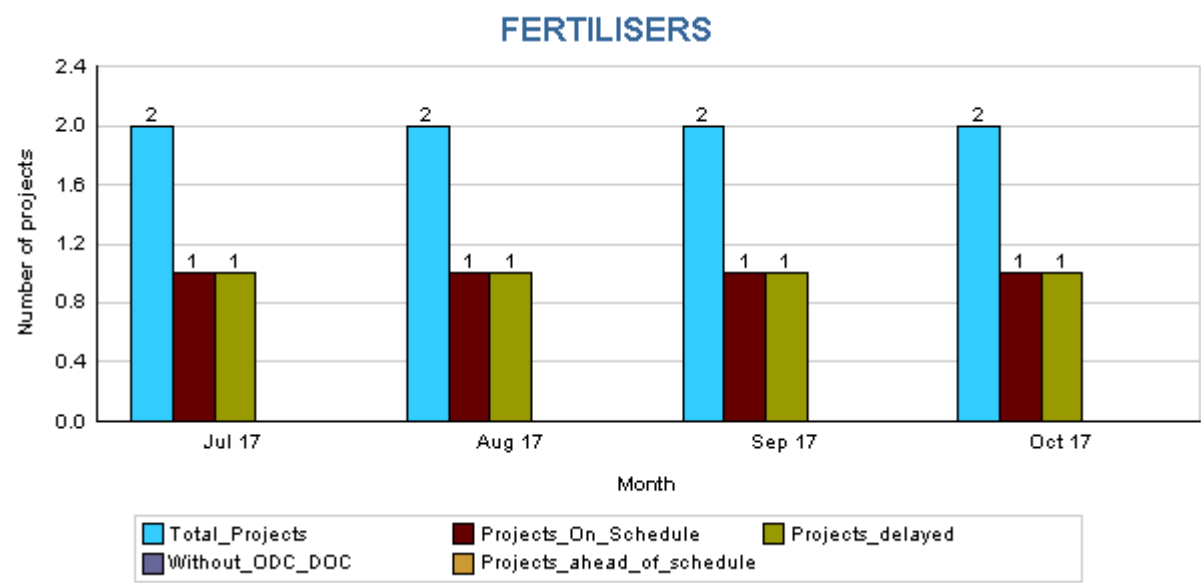


Break-up of 1 Delayed projects in October 2017



Delay in Months




Graphical Presentation of All Projects w.r.t. Original Schedule

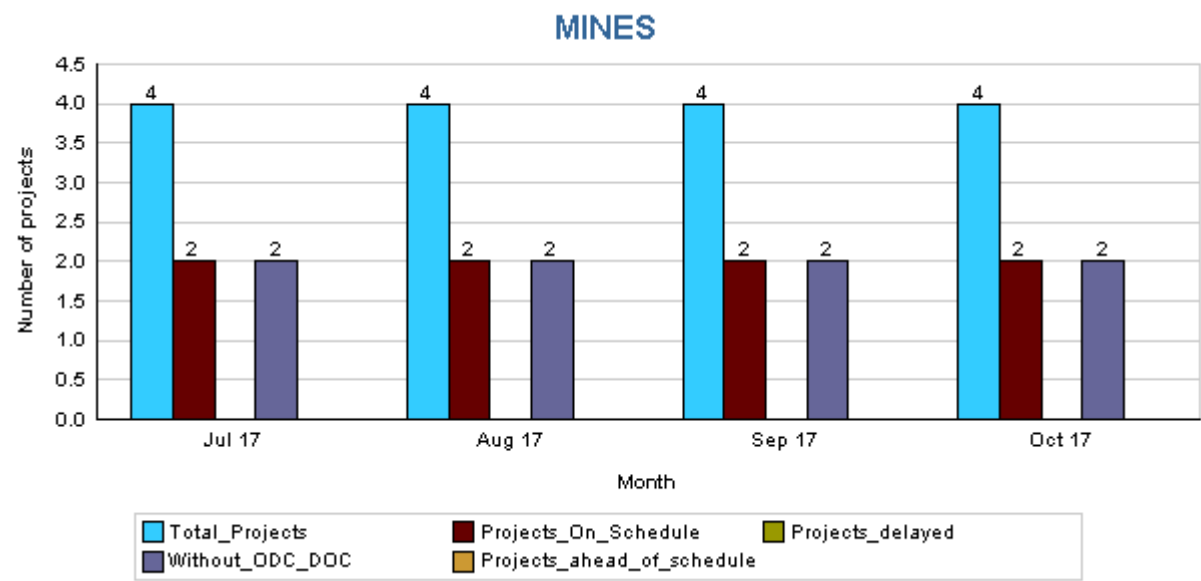


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

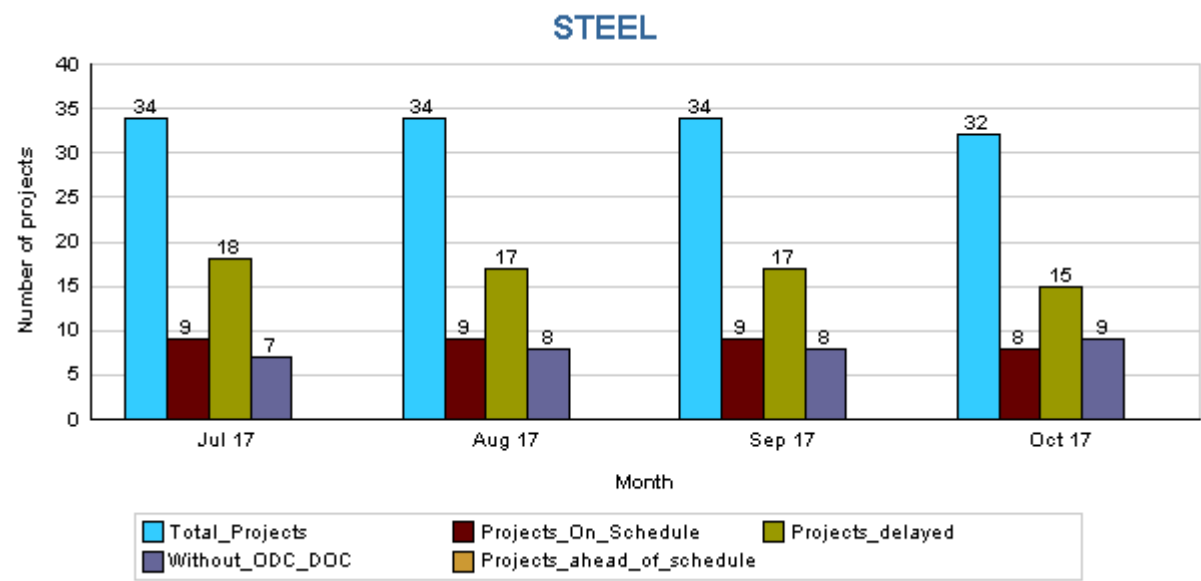

Break-up of 15 Delayed projects in October 2017

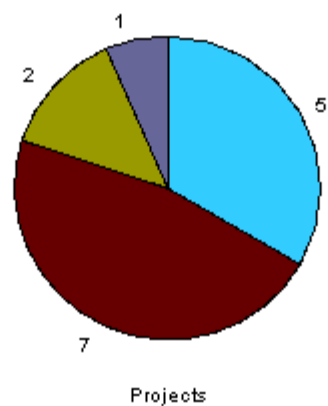


Delay in Months


Legend:

- 1-12 (Light Blue)
- 13-24 (Dark Red)
- 25-60 (Olive Green)
- 60 and Above (Purple)

Graphical Presentation of All Projects w.r.t. Original Schedule

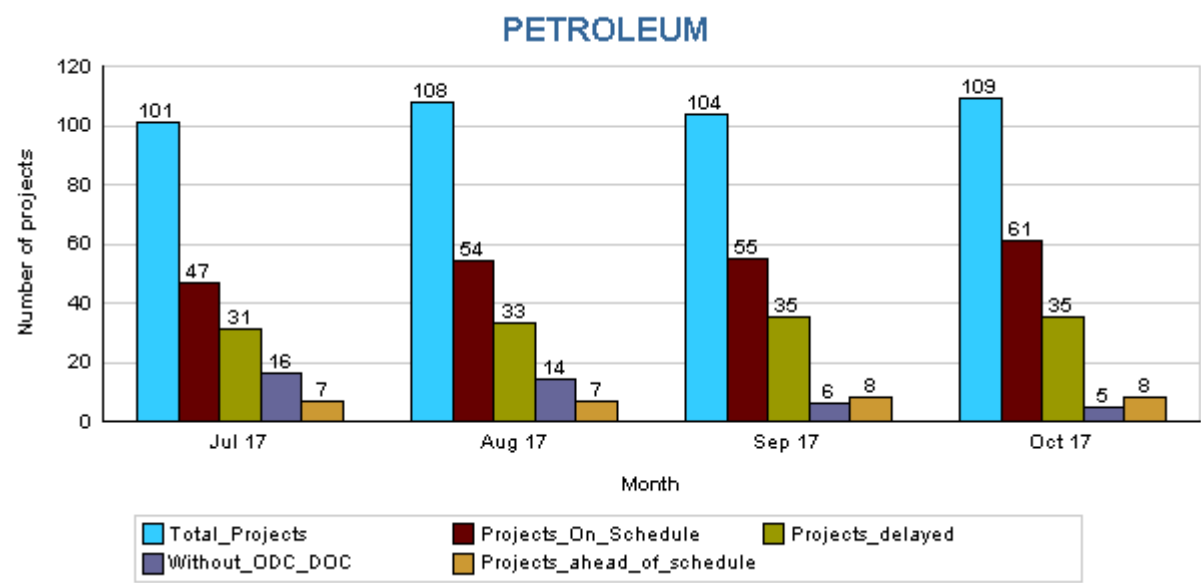


Break-up of 35 Delayed projects in October 2017

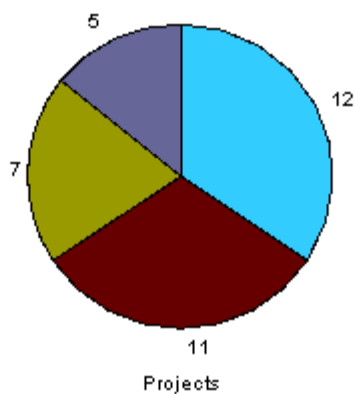


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

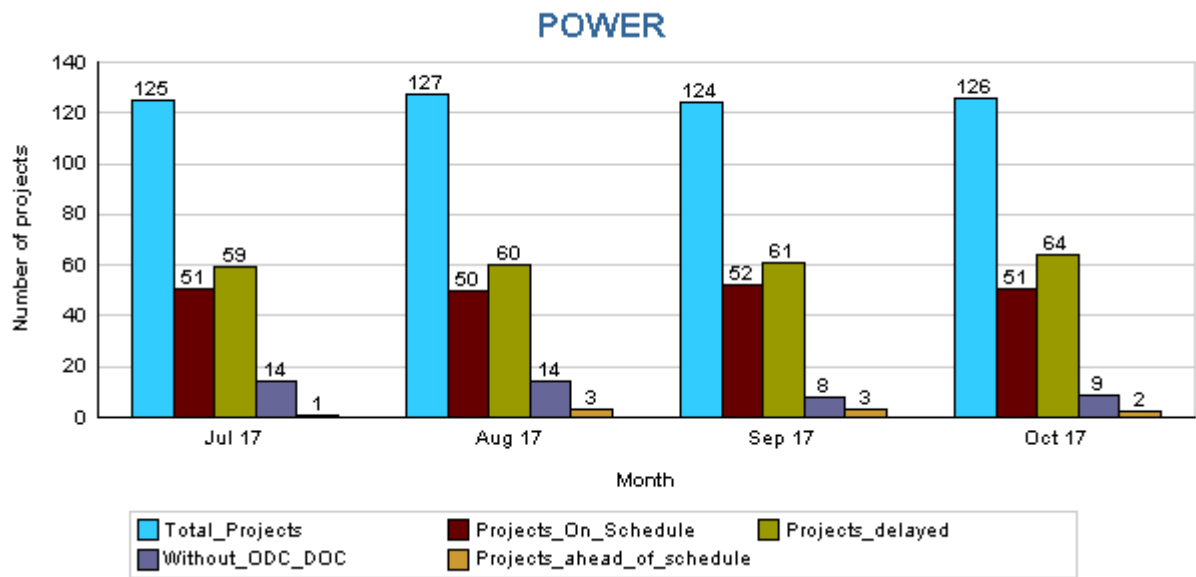


Break-up of 64 Delayed projects in October 2017

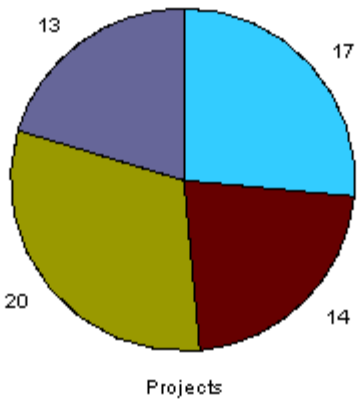


Delay in Months

1-12	13-24	25-60	60 and Above
------	-------	-------	--------------


Graphical Presentation of All Projects w.r.t. Original Schedule

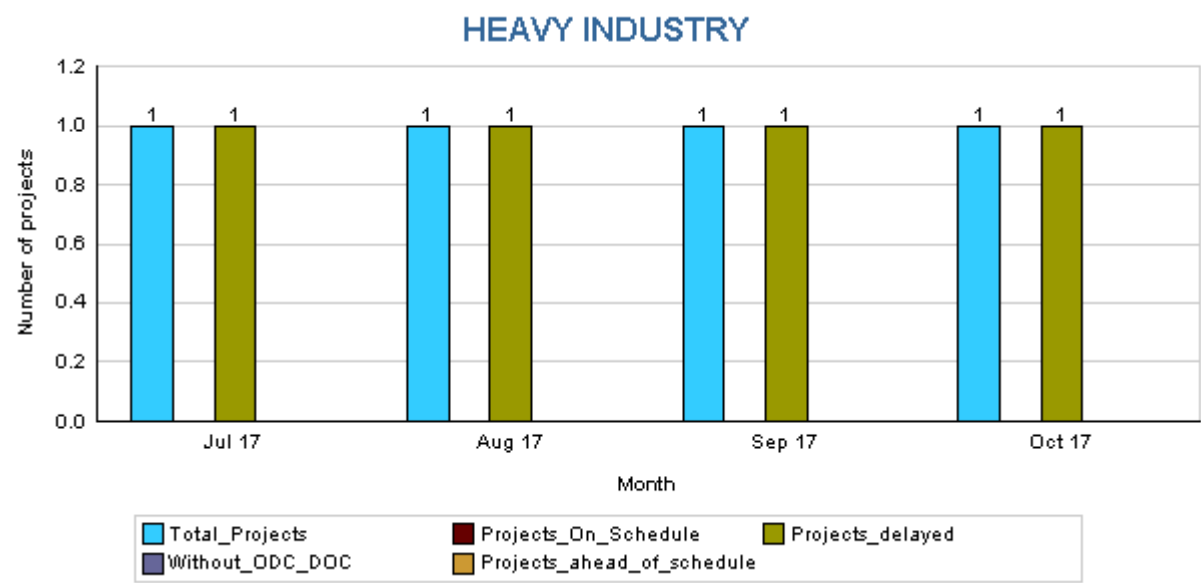


Break-up of 1 Delayed projects in October 2017

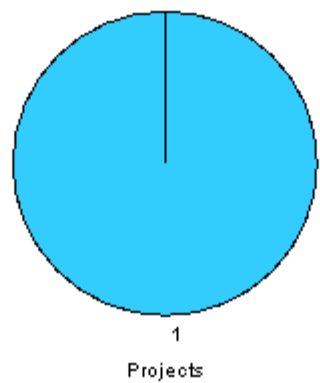


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

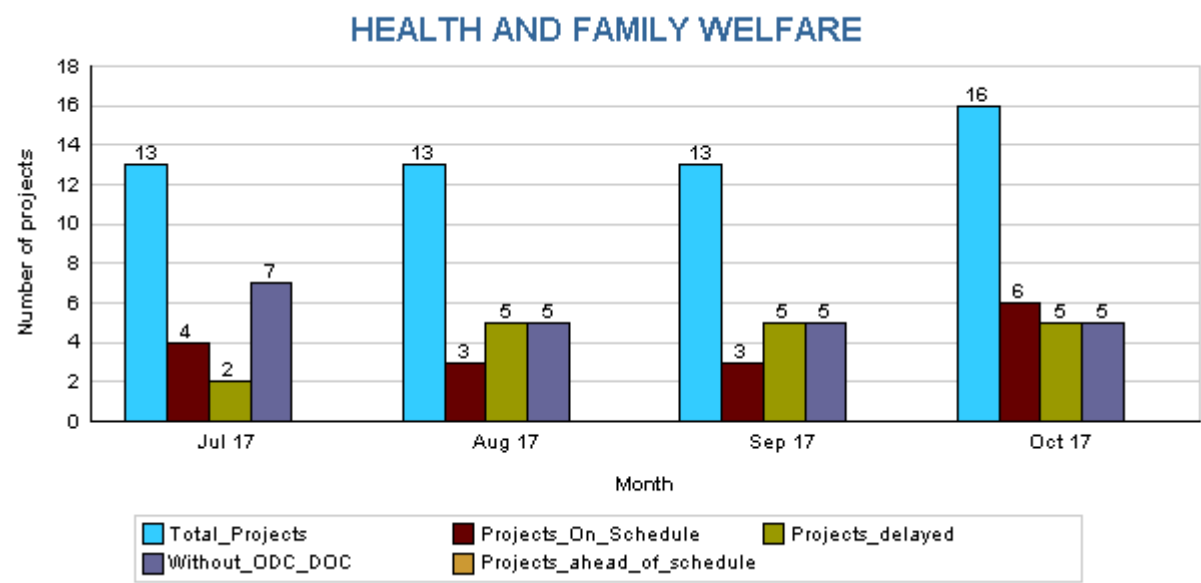


Break-up of 5 Delayed projects in October 2017

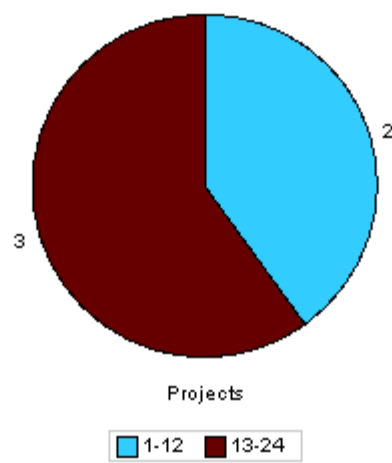


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

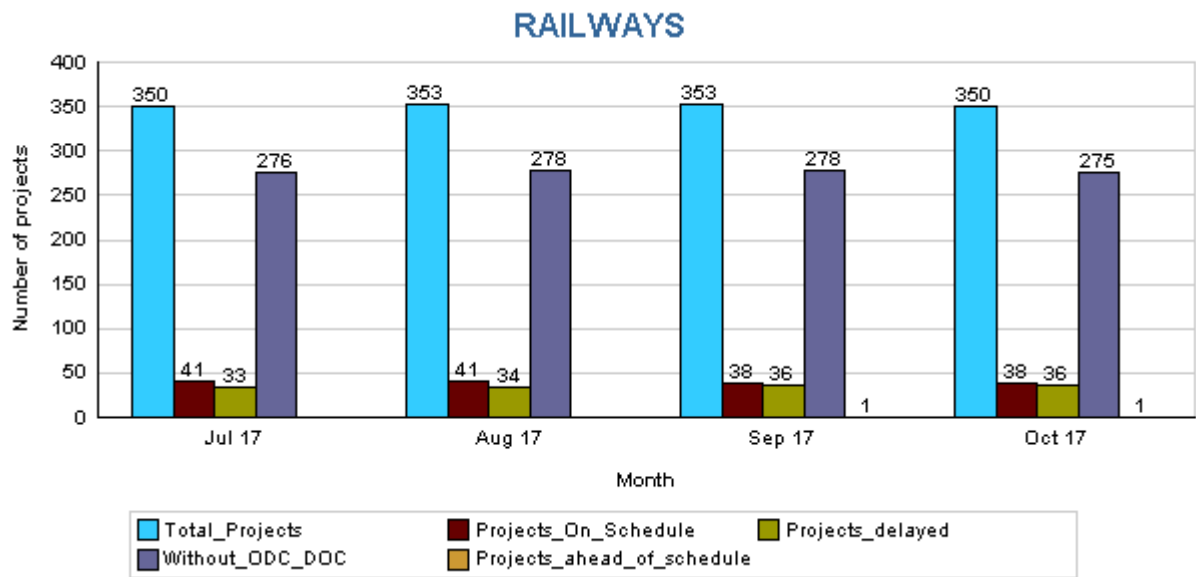


Break-up of 36 Delayed projects in October 2017

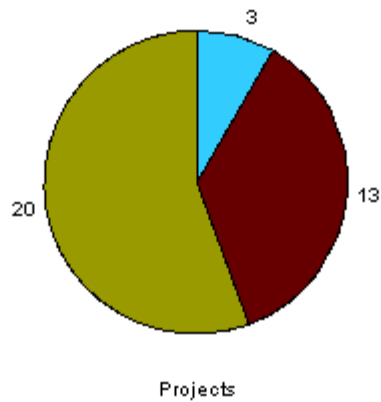


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

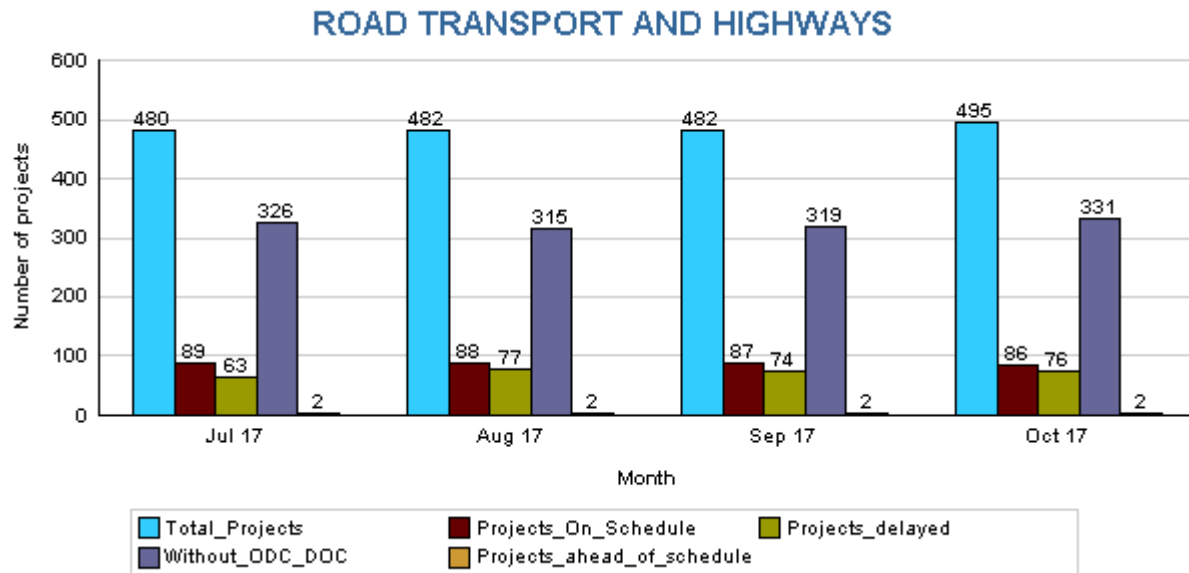


Break-up of 76 Delayed projects in October 2017

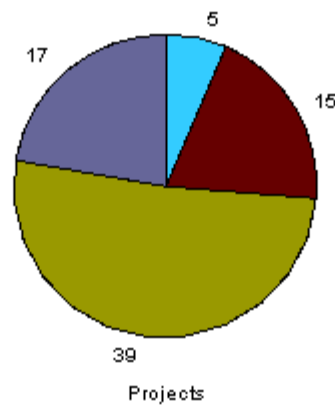


Delay in Months

Delay in Months	1-12	13-24	25-60	60 and Above
Projects	5	15	39	17


Graphical Presentation of All Projects w.r.t. Original Schedule

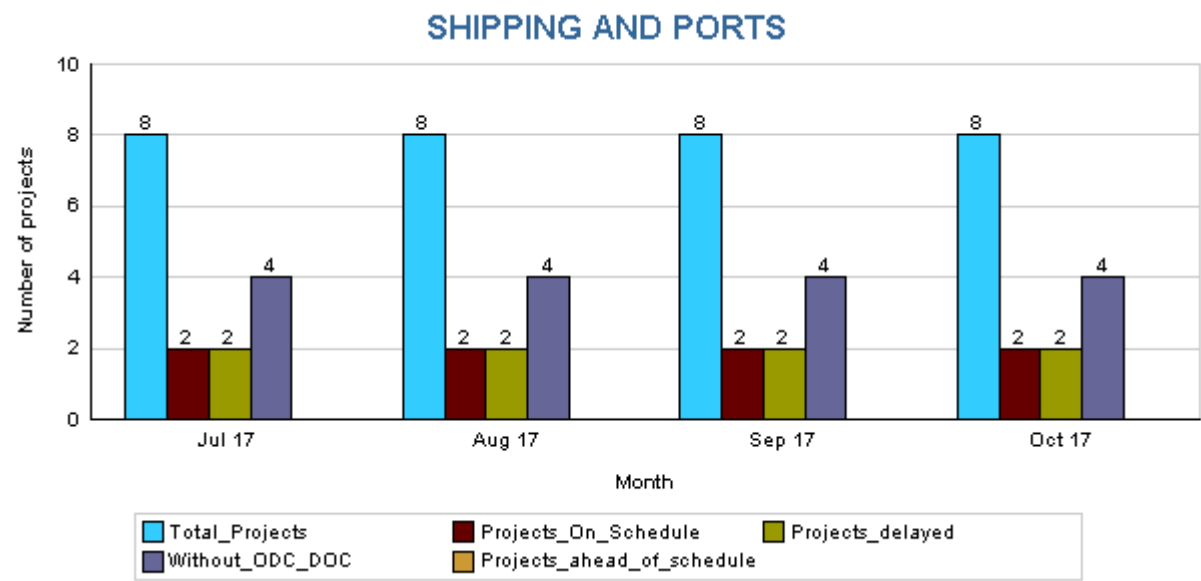


Break-up of 2 Delayed projects in October 2017

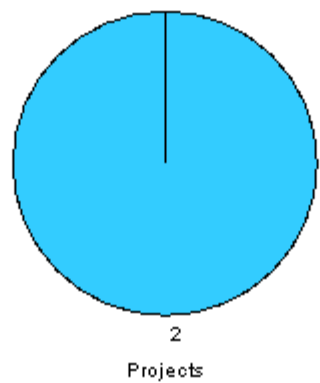


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

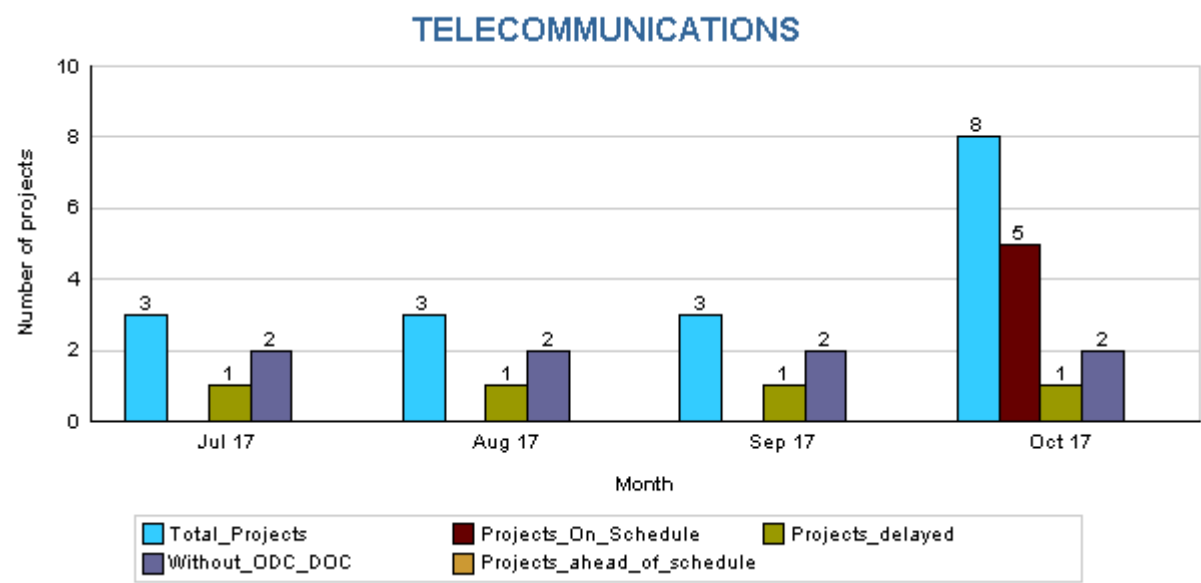


Break-up of 1 Delayed projects in October 2017

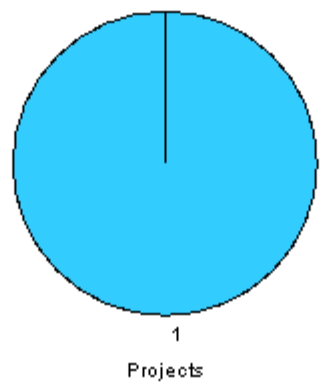

Delay in Months

25-60

Graphical Presentation of All Projects w.r.t. Original Schedule

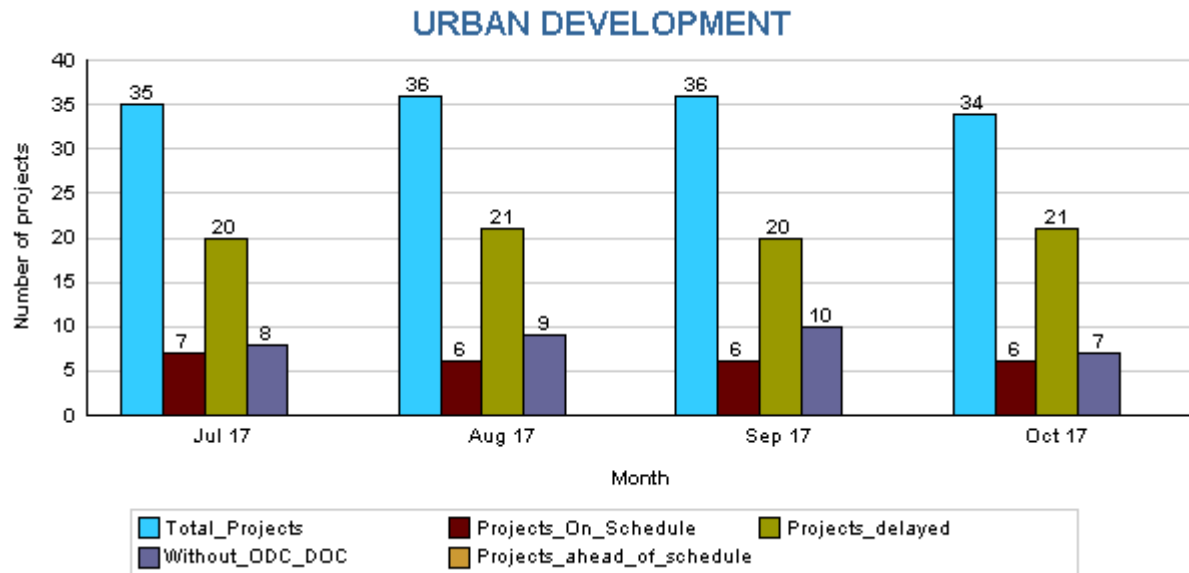


Break-up of 21 Delayed projects in October 2017



Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

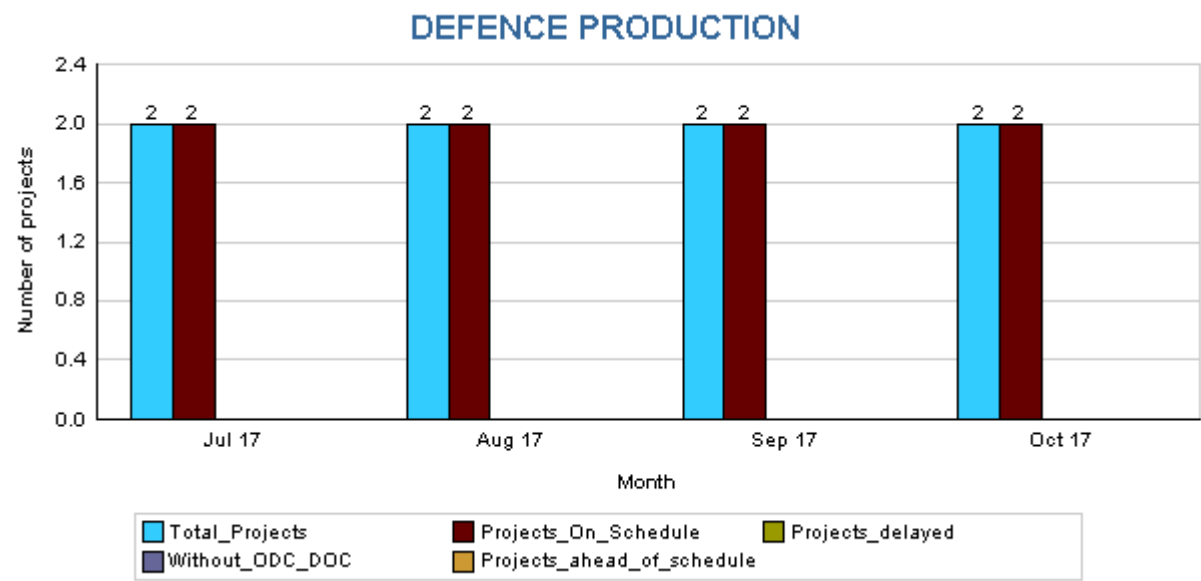

Delay in Months

TABLE-28

<u>Sector wise analysis of projects</u> Rs. 150 Crore and above					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	3	27,271.00	294,56.00	29,779.00	24,673.43
CIVIL AVIATION	2	624.07	6,24.07	994.86	549.39
COAL	91	87,760.24	880,21.45	88,310.52	21,074.07
FERTILISERS	2	680.64	6,92.29	703.44	482.90
MINES	4	6,773.63	67,73.63	6,773.63	916.01
STEEL	32	56,191.76	565,72.73	56,405.44	38,538.17
PETROLEUM	109	1,92,892.26	1,951,47.88	1,94,226.73	53,688.09
POWER	126	3,38,804.33	3,742,61.15	3,97,533.16	2,26,664.54
HEAVY INDUSTRY	1	1,718.00	17,18.00	3,827.30	2,289.00
HEALTH AND FAMILY WELFARE	16	4,538.61	45,38.61	4,550.91	1,865.48
RAILWAYS	350	3,53,681.04	3,771,57.73	4,65,297.26	1,38,934.44
ROAD TRANSPORT AND HIGHWAYS	495	3,27,076.22	3,276,50.24	3,33,448.42	83,379.52
SHIPPING AND PORTS	8	4,117.75	41,31.25	5,085.02	1,875.38
TELECOMMUNICATIONS	8	16,776.04	167,76.04	28,006.04	6,913.90
URBAN DEVELOPMENT	34	1,38,993.10	1,448,13.50	1,44,033.10	57,109.46
DEFENCE PRODUCTION	2	453.64	4,54.00	469.04	55.68
Grand total	1283	15,58,352.33	16,28,788.57	17,59,443.87	6,59,009.46

TABLE-29

Detail of ongoing Projects Costing Rs150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT , G	10/2009	11,459.00 -	11,459.00	10,775.00	12/2015 11/2016	11/2019	47(O) 36(R)	46/70
2	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN , G	10/2009	12,320.00 -	12,320.00	8,399.00	12/2016 03/2017	12/2020	48(O) 45(R)	34/68
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI, TAMIL NADU , G	09/2003	3,492.00 5,677.00	6,000.00	5,499.43	09/2010 09/2016	02/2018	89(O) 17(R)	83/87
	Total		27,271.00 -	29,779.00	24,673.43				163/225
	<u>CIVIL AVIATION</u>								
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT , PORTBLAIR - [N04000073]AAI, ANDAMAN & NICOBAR ISLANDS , G	10/2013	314.61 -	441.33	26.44	09/2018 -	06/2020	21(O) -	0/0
5	CONSTRUCTION OF NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT - [N04000050]AAI, SIKKIM , G	01/2009	309.46 -	553.53	522.95	01/2011 09/2017	10/2017	81(O) 1(R)	0/0
	Total		624.07 -	994.86	549.39				0/0
	<u>COAL</u>								
6	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL, CHHATISGARH , G	06/2010	11,816.40 -	11,816.40	2,519.20	03/2023 -	03/2023	0(O) -	13/17
7	KUSMUNDA EXPN. OCP (SECL) (15-50) MTY - [N06000008]SECL, CHHATISGARH , G	08/2013	7,612.33 -	7,612.33	1,369.37	03/2023 -	03/2023	0(O) -	3/19
8	PELMA OCP (15.00 MTY) - [N06000045]SECL, CHHATISGARH , G	11/2014	1,624.59 -	1,624.59	5.73	03/2023 -	03/2023	0(O) -	1/11
9	JAGANNATHPOR OCP (3.00 MTY) - [N06000075]SECL, CHHATISGARH , G	09/2008	152.43 459.49	459.49	80.16	03/2015 03/2020	03/2020	60(O) 0(R)	2/8
10	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH , G	07/2008	178.44 -	178.44	5.12	03/2014 -	03/2020	72(O) -	1/7
11	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH , G	12/2009	321.50 -	321.50	198.95	03/2014 -	03/2018	48(O) -	0/3
12	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL, CHHATISGARH , G	11/2009	198.59 -	198.59	169.49	03/2016 -	03/2018	24(O) -	6/8
13	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL, CHHATISGARH , G	04/2012	258.56 -	258.56	151.14	03/2016 -	03/2018	24(O) -	3/7
14	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL, CHHATISGARH , G	12/2013	610.63 -	610.63	28.74	03/2022 -	03/2022	0(O) -	1/8
15	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL, CHHATISGARH , G	05/2014	164.49 -	164.49	47.23	03/2020 -	03/2020	0(O) -	3/7
16	AMERA OC RCE - [N06000123]SECL, CHHATISGARH , G	02/2015	335.97 -	335.97	48.78	03/2018 -	03/2018	0(O) -	1/6

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
17	AMGAON OPENCAS T PROJECT RCE - [N06000135]SECL,CHHATISGARH , G	07/2015	316.10 -	316.10	38.29	03/2020 -	03/2020	0(O) -	0/5
18	DURGAPUR OPENCAS T PROJECT - [N06000136]SECL,CHHATISGARH , G	02/2015	916.24 -	916.24	.57	03/2023 -	03/2023	0(O) -	1/9
19	MADANNAGAR OPENCAS T PROJECT - [N06000140]SECL,CHHATISGARH , G	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024	0(O) -	0/3
20	VIJAY WEST OPENCAS T PROJECT - [N06000158]SECL,CHHATISGARH , G	05/2017	976.95 -	976.95	75.98	03/2026 -	03/2026	0(O) -	0/0
21	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND , G	08/2008	706.40 -	706.40	116.67	07/2012 03/2017	03/2021	104(O) 48(R)	2/4
22	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND , G	09/2009	153.82 -	153.82	127.71	03/2014 -	12/2017	45(O) -	4/6
23	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND , G	08/2007	163.51 -	163.51	93.28	03/2011 -	03/2020	108(O) -	2/4
24	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND , G	12/2007	179.87 -	179.87	97.03	03/2012 -	03/2019	84(O) -	2/4
25	PU RNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND , G	07/2008	210.98 -	210.98	206.80	03/2013 -	03/2018	60(O) -	3/4
26	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND , G	08/2008	264.68 -	264.68	153.27	03/2012 -	03/2019	84(O) -	2/4
27	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND , G	12/2009	510.85 -	510.85	341.12	03/2016 -	03/2018	24(O) -	2/4
28	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND , G	06/2009	162.46 -	162.46	80.63	03/2014 -	03/2019	60(O) -	2/4
29	MURAI DIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND , G	02/2011	339.88 -	339.88	12.08	04/2014 -	10/2018	54(O) -	4/7
30	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND , G	08/2011	1,230.27 -	1,230.27	198.90	04/2015 -	04/2019	48(O) -	2/6
31	AMRAPALI OC(12MTY) - [N06000103]CCL,JHARKHAND , G	02/2012	858.11 -	858.11	175.44	03/2020 -	03/2020	0(O) -	4/5
32	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND , G	02/2014	555.52 -	555.52	4.57	03/2021 -	03/2021	0(O) -	0/2
33	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND , G	08/2011	988.35 -	988.35	45.26	04/2017 -	-	-	1/3
34	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND , G	08/2010	289.45 -	289.45	152.06	05/2014 -	04/2018	47(O) -	0/8
35	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND , G	10/2012	269.82 -	269.82	150.11	04/2014 -	04/2018	48(O) -	0/10
36	HURA - C OC (3 MTY) - [N06000143]ECL,JHARKHAND , G	10/2015	359.69 -	359.69	7.61	03/2022 -	03/2022	0(O) -	0/21
37	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH , G	10/2007	259.40 -	486.57	296.40	03/2012 -	03/2018	72(O) -	1/3
38	BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH , G	08/2015	1,186.64 -	1,186.64	58.50	03/2023 -	03/2023	0(O) -	3/10
39	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH , G	02/2015	481.60 -	481.60	-	03/2023 -	03/2023	0(O) -	0/8
40	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH , G	12/2014	357.80 -	357.80	114.37	03/2021 -	03/2021	0(O) -	1/8
41	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH , G	12/2014	371.04 -	371.04	34.39	03/2021 -	03/2021	0(O) -	1/7

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
42	BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH , G	07/2015	231.92 -	231.92	-	03/2022 -	03/2022	0(O) -	1/6
43	MALACHUA OPENCAST PROJECT - [N06000139]SECL,MADHYA PRADESH , G	10/2015	488.33 -	488.33	1.06	03/2023 -	03/2023	0(O) -	0/4
44	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH , G	03/2016	869.44 -	869.44	111.56	03/2021 -	03/2021	0(O) -	1/3
45	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL,MADHYA PRADESH , G	07/2016	409.87 -	409.87	12.08	03/2022 -	03/2022	0(O) -	0/0
46	PENGANGA OCP(REVISED) - [N06000066]WCL,MAHARASHTRA , G	09/2014	441.82 -	441.82	174.80	03/2020 -	03/2020	0(O) -	6/11
47	DINESH OCP - [N06000118]WCL,MAHARASHTRA , G	11/2014	611.16 -	611.16	362.59	03/2020 -	03/2020	0(O) -	2/8
48	MAKARDHOKRA I OC - [N06000119]WCL,MAHARASHTRA , G	09/2014	266.23 -	266.23	138.85	03/2021 -	03/2021	0(O) -	7/12
49	GOKUL - [N06000120]WCL,MAHARASHTRA , G	11/2014	267.67 -	267.67	204.35	03/2018 -	03/2018	0(O) -	7/7
50	BHANEGAON OC - [N06000121]WCL,MAHARASHTRA , G	02/2015	187.94 409.68	409.68	72.23	03/2023 02/2017	03/2023	0(O) 73(R)	6/11
51	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA , G	05/2015	295.56 -	295.56	86.17	03/2019 -	03/2019	0(O) -	10/13
52	SINGHORI OC MINE - [N06000130]WCL,MAHARASHTRA , G	06/2015	205.49 -	205.49	69.58	03/2020 -	03/2020	0(O) -	5/10
53	AMALGAMATED PAUNI-II III OC MINE - [N06000131]WCL,MAHARASHTRA , G	06/2015	483.69 -	483.69	71.98	03/2021 -	03/2021	0(O) -	2/6
54	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]WCL,MAHARASHTRA , G	08/2015	727.28 -	727.28	229.90	03/2025 -	03/2025	0(O) -	3/13
55	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA , G	08/2015	288.90 -	288.90	-	03/2023 -	03/2023	0(O) -	2/10
56	KAMPTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA , G	11/2015	277.65 -	277.65	.13	03/2021 -	03/2021	0(O) -	2/6
57	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]WCL,MAHARASHTRA , G	11/2015	498.42 -	498.42	7.72	03/2020 -	03/2020	0(O) -	2/6
58	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL,MAHARASHTRA , G	02/2016	198.68 -	198.68	39.89	03/2019 -	03/2019	0(O) -	2/9
59	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA , G	02/2016	304.52 -	304.52	125.81	03/2019 -	03/2019	0(O) -	1/8
60	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]WCL,MULTI STATE , G	08/2016	319.76 -	319.76	.04	03/2022 -	03/2022	0(O) -	0/3
61	DHANKASA UG (1.00 MTY) - [N06000155]WCL,MULTI STATE , G	09/2016	458.07 -	458.07	-	03/2022 -	03/2022	0(O) -	0/12
62	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL,MULTI STATE , G	02/2017	328.00 -	328.00	45.31	03/2021 -	06/2022	15(O) -	1/6
63	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA , G	01/2005	302.96 -	302.96	329.10	03/2010 -	03/2018	96(O) -	9/10
64	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA , G	12/2007	490.10 -	490.10	278.35	03/2017 -	05/2018	14(O) -	11/12
65	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA , G	12/2007	457.77 -	457.77	404.99	03/2013 -	11/2018	68(O) -	8/9
66	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA , G	12/2007	172.08 -	172.08	191.37	03/2010 -	03/2019	108(O) -	3/4
67	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA , G	08/2008	207.28 -	207.28	223.25	03/2012 -	03/2019	84(O) -	4/5

Detail of ongoing Projects Costing Rs150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
68	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA , G	11/2008	479.53 -	479.53	219.23	03/2013 -	03/2019	72(O) -	5/8
69	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA , G	05/2014	479.15 -	479.15	20.80	03/2019 -	03/2019	0(O) -	2/9
70	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA , G	05/2014	3,756.36 -	3,756.36	682.14	03/2026 -	03/2026	0(O) -	3/15
71	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA , G	05/2014	337.66 -	337.66	29.74	03/2019 -	03/2019	0(O) -	3/6
72	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA , G	06/2014	289.03 -	289.03	-	03/2018 -	03/2018	0(O) -	2/5
73	GARJANBAHAL OCP - [N06000117]MCL,ODISHA , G	11/2014	1,375.38 -	1,375.38	369.08	03/2021 -	03/2021	0(O) -	2/9
74	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN , Central Sector Projects	03/2015	522.45 -	522.45	5.65	09/2019 -	09/2019	0(O) -	0/0
75	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN , Central Sector Projects	03/2015	513.63 -	513.63	167.04	12/2019 -	12/2019	0(O) -	0/0
76	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU , G	06/2011	5,907.11 -	5,907.11	4,834.48	12/2015 04/2018	04/2018	28(O) 0(R)	16/35
77	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU , G	04/2013	1,458.17 709.06	709.06	302.65	06/2015 09/2019	09/2019	51(O) 0(R)	3/7
78	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]NLC,TAMIL NADU , G	05/2016	687.28 830.45	830.45	705.43	06/2017 -	10/2017	4(O) -	0/0
79	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA , G	10/2006	249.03 448.86	448.86	162.30	03/2012 -	03/2019	84(O) -	32/42
80	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA , G	12/2008	453.63 -	453.63	121.91	12/2012 -	-	-	11/44
81	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA , G	12/2009	418.97 -	489.62	48.58	03/2012 -	03/2023	132(O) -	0/2
82	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA , G	03/2010	209.78 -	209.78	143.08	03/2015 -	03/2018	36(O) -	29/31
83	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA , G	03/2010	181.19 -	181.19	159.87	03/2012 -	03/2018	72(O) -	5/6
84	KISTARAM OCP - [N06000089]SCCL,TELANGANA , G	11/2010	242.29 164.04	164.04	.34	03/2015 -	03/2020	60(O) -	0/5
85	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA , G	07/2011	162.76 349.28	349.28	1.31	03/2015 -	03/2020	60(O) -	4/29
86	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA , G	07/2011	447.06 -	437.51	259.34	03/2015 -	03/2021	72(O) -	5/13
87	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA , G	06/2012	365.01 -	365.01	83.80	06/2015 -	03/2018	33(O) -	27/36
88	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA , G	07/2012	417.33 417.33	417.33	59.26	07/2016 -	03/2020	44(O) -	19/28
89	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA , G	11/2012	430.45 415.37	415.37	143.67	03/2016 -	03/2018	24(O) -	33/39
90	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]SCCL,TELANGANA , G	05/2015	397.09 442.42	442.42	25.07	03/2019 -	03/2019	0(O) -	6/18
91	KOYAGUDEM OPENCAST PROJECT - [N06000146]SCCL,TELANGANA , Central Sector Projects	10/2015	426.79 -	426.79	-	03/2018 -	03/2019	12(O) -	0/9
92	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]SCCL,TELANGANA , G	12/2015	477.65 -	477.65	-	03/2020 -	03/2020	0(O) -	1/17

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
93	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]NCL,UTTAR PRADESH , G	06/2011	1,131.28 -	1,131.28	430.95	03/2018 -	03/2018	0(O) -	6/10
94	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH , G	07/2016	17,237.00 -	17,237.80	1,123.80	11/2021 -	11/2021	0(O) -	0/0
95	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]ECL,WEST BENGAL , G	11/2015	602.86 -	602.86	271.12	03/2022 -	03/2022	0(O) -	6/12
96	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL , G	08/2012	1,055.05 -	1,055.05	317.37	03/2018 -	03/2020	24(O) -	8/15
	Total		87,760.24 -	88,310.52	21,074.07				394/904
	<u>FERTILISERS</u>								
97	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA , G	10/2014	197.79 209.44	209.44	82.72	11/2016 04/2019	04/2019	29(O) 0(R)	0/0
98	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]RCF,MAHARASHTRA , G	02/2016	482.85 -	494.00	400.18	12/2017 -	12/2017	0(O) -	0/1
	Total		680.64 -	703.44	482.90				0/1
	<u>MINES</u>								
99	Implementation of 50.4 MW Wind Power Project at Jath, Sangli, Maharashtra - [N10000008]NALCO,MAHARASHTRA , Private	12/2015	355.13 -	355.13	355.13	11/2016 12/2016	12/2016	-	1/1
100	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]NALCO,ODISHA , G	12/2014	5,540.00 5,540.00	5,540.00	23.84	04/2021 04/2021	04/2021	0(O) 0(R)	1/2
101	UTKAL D AND E COAL BLOCK - [N10000011]NALCO,ODISHA , G	05/2016	534.00 534.00	534.00	192.54	01/2020 01/2020	01/2020	0(O) 0(R)	1/2
102	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT RAJASTHAN - [N10000009]NALCO,RAJASTHAN , PPP (ANNUITY)	12/2015	344.50 344.50	344.50	344.50	11/2016 11/2016	11/2016	-	1/1
	Total		6,773.63 -	6,773.63	916.01				4/6
	<u>STEEL</u>								
103	3RD CONVERTER AND 4TH CASTER - [N12000088]RINL,ANDHRA PRADESH , G	07/2011	974.76 -	974.76	586.93	07/2016 -	11/2017	16(O) -	1/1
104	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH , G	12/2009	343.00 -	488.40	227.98	10/2016 -	03/2018	17(O) -	0/0
105	CONSTRUCTION OF 123 BLOCKS IN TELEGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH , G	07/2014	232.00 -	232.00	-	01/1999 -	-	-	0/0
106	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH , G	12/2011	2,858.00 -	2,500.00	621.35	12/2017 -	10/2018	10(O) -	0/0
107	CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH , G	08/2015	320.66 -	320.66	17.71	08/2018 -	08/2018	0(O) -	0/0
108	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120]RINL,ANDHRA PRADESH , G	07/2015	465.85 -	465.85	41.38	07/2018 -	07/2018	0(O) -	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
109	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR , G	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72(O) -	0/0
110	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH , G	08/2010	17,265.00 -	17,265.00	18,052.70	03/2013 -	12/2017	57(O) -	35/38
111	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH , G	04/2014	188.93 -	188.93	114.49	04/2015 -	-	-	4/5
112	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH , G	01/2010	15,525.00 -	15,525.00	12,854.06	05/2015 10/2018	10/2018	41(O) 0(R)	54/86
113	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115]NMDC,CHHATISGARH , G	11/2015	818.00 -	818.00	28.13	06/2020 -	06/2020	0(O) -	4/12
114	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL,GUJARAT , G	01/2013	175.00 -	175.00	1.83	- -	12/2017	- -	0/0
115	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND , G	10/2013	245.67 -	245.67	196.21	05/2016 -	11/2017	18(O) -	2/3
116	ALTERNATE GAS NETWORK AT BSL - [N12000093]SAIL,JHARKHAND , G	03/2015	255.19 -	255.19	168.02	03/2018 -	03/2018	0(O) -	1/2
117	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND , G	03/2015	1,034.01 -	1,034.01	194.21	10/2017 -	07/2018	9(O) -	0/2
118	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND , G	05/2015	1,154.18 -	1,154.18	477.34	12/2017 -	05/2018	5(O) -	1/2
119	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND , G	02/2014	4,749.00 -	4,749.00	70.54	09/2017 -	-	-	0/0
120	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND , G	12/2007	253.92 253.92	253.92	193.97	06/2016 -	03/2018	21(O) -	0/0
121	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND , G	12/2007	200.00 -	200.00	131.15	03/2018 -	03/2018	0(O) -	0/0
122	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND , G	02/2014	787.29 -	787.29	285.30	12/2016 -	12/2018	24(O) -	0/0
123	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND , G	04/2013	170.00 -	170.00	88.91	04/2018 -	04/2018	0(O) -	0/0
124	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND , G	11/2016	262.87 -	262.87	37.19	06/2019 -	06/2019	0(O) -	0/1
125	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA , G	05/2005	768.88 1,070.97	1,113.34	1,085.64	02/2014 -	-	-	0/0
126	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA , G	07/2011	324.87 324.87	324.87	262.93	12/2015 -	-	-	0/0
127	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA , G	04/2014	151.33 -	151.33	7.15	09/2017 -	12/2018	15(O) -	0/0
128	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA , G	04/2015	3,127.30 -	3,127.30	1,380.44	04/2018 -	02/2019	10(O) -	1/3

Detail of ongoing Projects Costing Rs150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
129	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN , G	05/2015	189.00 -	189.00	-	03/2017 -	08/2018	17(O) -	0/0
130	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA , G	03/2007	149.73 173.00	175.94	178.65	12/2015 -	-	-	0/0
131	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA , G	12/2007	202.61 227.00	227.00	199.95	12/2016 -	12/2017	12(O) -	0/0
132	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA , G	10/2011	175.49 206.71	206.71	141.28	12/2016 -	-	-	0/0
133	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH , G	04/2014	1,682.85 -	1,682.85	63.22	09/2018 -	09/2018	0(O) -	0/0
134	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL , Central Sector Projects	08/2012	185.37 -	185.37	178.30	03/2016 -	-	-	0/0
	Total		56,191.76 -	56,405.44	38,538.17				103/155
	<u>PETROLEUM</u>								
135	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH , G	07/2016	20,928.00 -	20,928.00	540.49	07/2020 -	07/2020	0(O) -	0/0
136	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]HPCL,ANDHRA PRADESH , G	09/2016	407.00 -	407.00	30.61	09/2019 -	09/2019	0(O) -	15/27
137	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH , G	03/2016	34,012.00 -	34,012.00	253.97	06/2020 06/2020	06/2020	0(O) 0(R)	0/0
138	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL,ANDHRA PRADESH , G	01/2015	342.00 -	342.00	-	03/2021 -	03/2021	0(O) -	0/0
139	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL,ANDHRA PRADESH , G	07/2014	247.00 -	247.00	-	03/2021 -	03/2021	0(O) -	0/0
140	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]ONGC,ANDHRA PRADESH , G	04/2017	420.76 -	420.76	-	09/2018 09/2018	09/2018	0(O) 0(R)	0/0
141	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216]IOCL,ARUNACHAL PRADESH , G	01/2016	247.52 -	247.52	53.50	02/2019 -	12/2018	-2(O) -	2/10
142	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM , G	03/2009	2,465.15 -	2,378.89	2,060.68	03/2013 09/2018	09/2018	66(O) 0(R)	5/15
143	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM , G	06/2010	202.94 341.70	330.35	3.14	01/2014 11/2019	11/2019	70(O) 0(R)	0/2
144	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM , G	03/2009	228.64 -	209.19	147.06	12/2016 -	03/2018	15(O) -	0/0
145	DIESEL HYDROTREATOR - [N16000207]NRL,ASSAM , Central Sector Projects	07/2015	1,031.37 -	1,031.37	305.91	01/2018 -	01/2018	0(O) -	46/61

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
146	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM , G	06/2016	423.00 -	423.00	91.45	08/2019 -	08/2019	0(O) -	2/13
147	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]IOCL,ASSAM , G	02/2016	2,582.00 -	2,582.00	250.76	11/2019 -	11/2019	0(O) -	0/0
148	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]ONGC,ASSAM , G	07/2016	249.85 250.00	244.70	-	05/2020 05/2020	05/2020	0(O) 0(R)	0/0
149	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM , G	09/2012	871.35 -	1,200.00	958.50	03/2015 -	11/2017	32(O) -	0/5
150	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]IOCL,BIHAR , G	07/2015	822.66 -	822.66	223.14	11/2018 -	11/2018	0(O) -	0/0
151	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]IOCL,BIHAR , G	05/2016	664.00 -	664.00	147.71	12/2020 -	02/2020	-10(O) -	0/2
152	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]IOCL,BIHAR , G	09/2015	324.00 -	324.00	1.48	06/2020 -	06/2020	0(O) -	2/2
153	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI , G	08/2014	6,086.08 -	5,479.75	2,148.82	05/2019 10/2019	10/2019	5(O) 0(R)	0/0
154	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT , G	09/2011	202.25 -	160.16	106.98	07/2016 06/2018	06/2018	23(O) 0(R)	5/12
155	GAMJI REDEVELOPMENT PROJECT - [N16000202]ONGC,GUJARAT , G	05/2015	1,671.22 567.22	567.22	347.69	11/2019 12/2018	12/2018	-11(O) 0(R)	0/0
156	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]ONGC,GUJARAT , Central Sector Projects	11/2014	195.63 -	187.10	139.30	09/2018 09/2018	09/2018	0(O) 0(R)	0/0
157	ANKLESHWAR BARODA PIPELINE PROJECT - [N16000232]GAIL,GUJARAT , G	07/2014	199.95 -	199.95	121.90	03/2018 -	03/2018	0(O) -	16/22
158	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT , G	04/2016	327.78 -	200.00	15.19	04/2018 -	04/2018	0(O) -	15/20
159	FUEL QUALITY UPGRADATION (DHDT/DHDS) PROJECT AT GUJARAT REFINERY - [N16000245]IOCL,GUJARAT , G	02/2016	931.00 -	931.00	400.75	07/2017 -	02/2018	7(O) -	0/0
160	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]ONGC,GUJARAT , G	02/2017	1,162.56 1,162.56	1,162.56	196.84	03/2026 03/2026	03/2026	0(O) 0(R)	0/0
161	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]IOCL,GUJARAT , Central Sector Projects	09/2016	208.35 -	208.35	16.93	07/2020 -	07/2020	0(O) -	0/0
162	REPLACEMENT OF KV SECTION OF KSPL - [N16000287]IOCL,GUJARAT , Central Sector Projects	10/2014	279.00 -	279.00	-	08/2018 -	08/2017	-	0/0
163	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP - [N16000226]IOCL,HIMACHAL PRADESH , G	02/2016	356.00 -	356.00	72.34	05/2019 -	12/2018	-5(O) -	1/13
164	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]IOCL,HIMACHAL PRADESH , G	02/2016	151.00 -	151.00	-	09/2019 -	09/2019	0(O) -	2/2
165	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND , G	04/2011	191.96 -	191.96	176.28	05/2015 06/2017	06/2017	-	8/12
166	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]ONGC,JHARKHAND , G	12/2015	658.62 910.23	910.23	5.22	03/2023 03/2022	03/2022	-12(O) 0(R)	0/0
167	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KARNATAKA , G	01/2006	993.00 -	1,693.00	1,544.61	01/2012 -	11/2017	70(O) -	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
168	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA , Central Sector Projects	02/2015	749.00 -	749.00	504.66	02/2020 -	02/2020	0(O) -	0/0
169	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]MANGALORE REFIN,KARNATAKA , G	05/2015	224.00 207.00	207.25	42.14	04/2019 -	04/2019	0(O) -	5/8
170	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]MANGALORE REFIN,KARNATAKA , G	10/2015	135.00 170.70	170.70	81.39	03/2019 -	03/2019	0(O) -	3/11
171	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA , G	09/2016	1,810.00 1,810.00	1,810.00	52.96	12/2019 -	12/2019	0(O) -	6/9
172	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA , G	10/2015	607.06 714.25	714.25	276.85	10/2017 -	03/2019	17(O) -	36/52
173	PALAKKAD LPG PLANT - [N16000225]BPCL,KERALA , G	02/2015	184.00 -	184.00	81.68	12/2017 -	12/2017	0(O) -	0/10
174	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA , G	11/2014	4,588.29 5,245.96	4,588.29	927.73	08/2018 05/2019	05/2019	9(O) 0(R)	0/20
175	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA , G	02/2016	3,313.00 -	3,313.00	65.92	02/2020 -	02/2020	0(O) -	0/0
176	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT KOCHI REFINERY - [N16000264]BPCL,KERALA , G	05/2015	337.06 -	337.06	20.75	08/2018 -	08/2018	0(O) -	0/0
177	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]ONGC,MADHYA PRADESH , Central Sector Projects	03/2009	181.02 -	173.28	127.44	01/2017 03/2018	03/2018	14(O) 0(R)	0/0
178	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA , G	03/2011	861.79 1,256.72	1,256.72	1,170.49	05/2013 12/2017	12/2017	55(O) 0(R)	1/5
179	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA , G	12/2011	2,059.63 -	2,665.65	1,650.87	03/2015 03/2018	03/2018	36(O) 0(R)	0/17
180	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA , G	03/2012	2,592.17 -	2,592.17	2,040.89	05/2014 05/2018	05/2018	48(O) 0(R)	0/21
181	MH NORTH REDEVELOPMENT PHASE III - [N16000188]ONGC,MAHARASHTRA , G	06/2014	5,706.47 5,813.25	5,813.25	5,554.21	05/2017 05/2018	05/2018	12(O) 0(R)	7/16
182	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA , G	11/2014	6,068.80 6,068.80	5,296.93	4,250.08	04/2019 03/2019	03/2019	-1(O) 0(R)	0/0
183	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC,MAHARASHTRA , G	02/2015	2,899.93 -	2,098.43	1,237.43	05/2017 05/2018	05/2018	12(O) 0(R)	0/0
184	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA , G	08/2015	2,818.88 -	2,818.88	338.56	03/2019 05/2020	05/2020	14(O) 0(R)	0/0
185	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]ONGC,MAHARASHTRA , Central Sector Projects	01/2015	4,619.94 -	3,961.54	3,424.59	12/2017 03/2019	03/2019	15(O) 0(R)	0/0
186	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA , Central Sector Projects	12/2015	3,190.69 -	3,247.19	864.69	04/2018 04/2018	04/2018	0(O) 0(R)	0/0
187	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL,MAHARASHTRA , G	05/2016	1,945.00 -	1,945.00	72.56	08/2021 -	08/2021	0(O) -	1/2

Detail of ongoing Projects Costing Rs150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
188	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]BPCL,MAHARASHTRA , G	02/2016	554.00 -	554.00	25.73	02/2020 -	01/2021	11(O) -	0/0
189	MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL,MAHARASHTRA , G	04/2013	449.58 -	449.58	97.27	12/2019 -	12/2019	0(O) -	0/0
190	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY - [N16000262]BPCL,MAHARASHTRA , G	05/2015	193.40 -	193.40	8.55	01/2019 -	01/2019	0(O) -	0/0
191	ADDITIONAL FACILITIES AT MANMAD FOR COVERSON TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA , G	05/2016	212.00 -	212.00	.08	01/2021 -	01/2021	0(O) -	0/0
192	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA , G	05/2016	348.00 -	348.00	.05	01/2021 -	01/2021	0(O) -	0/0
193	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELI - [N16000276]IOCL,MAHARASHTRA , G	05/2016	261.00 -	261.00	.05	01/2021 -	01/2021	0(O) -	0/0
194	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL,MAHARASHTRA , Central Sector Projects	09/2015	4,199.00 -	4,199.00	194.97	03/2020 -	07/2019	-8(O) -	0/0
195	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY - [N16000290]ONGC,MAHARASHTRA , Central Sector Projects	01/2017	474.15 -	474.15	110.96	05/2019 -	05/2019	0(O) -	0/0
196	DEVELOPMENT OF B-147 FIELD - [N16000292]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	546.15 -	546.15	-	11/2019 -	11/2019	0(O) -	0/0
197	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	511.30 -	511.30	-	11/2019 -	11/2019	0(O) -	0/0
198	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	968.61 -	968.61	-	11/2019 -	11/2019	0(O) -	0/0
199	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE , G	03/2015	3,957.00 3,561.00	3,397.00	1,399.57	12/2018 -	12/2018	0(O) -	27/39
200	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE , G	06/2007	736.65 -	571.47	542.29	09/2011 06/2019	06/2019	93(O) 0(R)	0/0
201	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE , G	08/2009	1,793.00 -	1,793.00	1,788.86	12/2016 06/2017	06/2017	-	8/8
202	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE , G	04/2012	600.17 -	600.17	657.00	12/2014 03/2018	03/2018	39(O) 0(R)	0/8
203	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE , G	02/2011	913.00 1,330.00	1,330.00	1,036.41	06/2018 -	06/2018	0(O) -	1/1
204	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE , G	12/2009	309.81 723.40	723.40	394.90	10/2014 03/2018	03/2018	41(O) 0(R)	29/40
205	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE , G	07/2011	352.56 -	439.03	126.43	03/2017 -	11/2018	20(O) -	0/0
206	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE , G	05/2013	4,124.35 4,259.59	5,637.00	3,947.52	04/2016 12/2017	12/2017	20(O) 0(R)	0/3

Detail of ongoing Projects Costing Rs150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
207	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE , G	01/2015	1,823.00 -	1,823.00	41.75	12/2020 -	12/2020	0(O) -	0/0
208	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE , G	01/2015	2,321.00 -	2,321.00	55.55	12/2020 -	08/2020	-4(O) -	0/2
209	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE , G	02/2015	890.00 -	887.00	223.15	10/2019 -	10/2019	0(O) -	2/3
210	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE , G	01/2015	690.00 -	690.00	133.80	07/2018 06/2020	06/2020	23(O) 0(R)	10/36
211	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]HPCL,MULTI STATE , G	09/2016	1,879.00 -	1,879.00	209.30	06/2020 -	06/2020	0(O) -	7/24
212	RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB,HARYANA) - [N16000242]HPCL,MULTI STATE , G	11/2016	230.00 -	230.00	13.37	02/2019 -	02/2019	0(O) -	5/13
213	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE , G	05/2016	406.00 -	406.00	.50	10/2020 -	10/2020	0(O) -	0/0
214	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE , G	09/2016	571.66 -	571.66	-	12/2019 -	12/2019	0(O) -	0/0
215	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE , G	07/2015	2,881.40 -	2,881.40	9.98	12/2019 -	12/2019	0(O) -	0/24
216	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]GAIL,MULTI STATE , G	03/2017	2,250.00 -	2,250.00	4.87	12/2019 -	12/2019	0(O) -	0/24
217	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]GAIL,MULTI STATE , G	03/2017	3,212.00 -	3,212.00	1.47	12/2020 -	12/2020	0(O) -	0/24
218	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE , Central Sector Projects	06/2009	2,915.00 -	2,915.00	1,269.70	12/2012 -	02/2019	74(O) -	3/42
219	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA , G	03/2014	3,150.00 -	3,150.00	1,308.04	09/2017 12/2018	12/2018	15(O) 0(R)	5/6
220	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]IOCL,ODISHA , G	03/2014	238.50 -	238.50	167.48	03/2017 10/2017	10/2017	7(O) 0(R)	6/6
221	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]GAIL,ODISHA , G	03/2017	2,253.00 -	2,253.00	12.88	12/2019 -	12/2019	0(O) -	0/24
222	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]IOCL,ODISHA , G	05/2016	429.00 -	429.00	39.02	01/2019 -	01/2019	0(O) -	0/0
223	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA , Central Sector Projects	12/2016	161.59 -	161.59	28.80	12/2019 -	12/2019	0(O) -	0/0
224	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL,ODISHA , Central Sector Projects	07/2017	268.79 -	268.79	1.21	07/2022 -	07/2022	0(O) -	0/0
225	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN , G	11/2011	310.00 -	370.00	17.84	03/2013 -	-	-	0/24
226	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU , G	05/2013	711.00 -	711.00	11.12	06/2020 -	06/2020	0(O) -	0/0
227	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU , G	03/2013	3,110.36 -	3,110.36	2,863.96	11/2015 -	12/2017	25(O) -	51/52

Detail of ongoing Projects Costing Rs150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
228	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL,TAMIL NADU , G	05/2015	257.87 -	257.87	139.96	11/2016 -	02/2018	15(O) -	18/22
229	DHDS REVAMP FOR MEETING BS-IV DIESEL QUALITY - [N16000218]CPCL,TAMIL NADU , Central Sector Projects	02/2016	367.11 -	367.11	225.34	04/2017 -	12/2017	8(O) -	21/22
230	ENNORE TERMINAL - [N16000224]BPCL,TAMIL NADU , G	08/2014	393.00 -	393.00	211.60	04/2018 -	04/2018	0(O) -	0/10
231	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU , G	11/2012	678.00 -	678.00	5.08	02/2017 -	-	-	0/0
232	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU , G	11/2015	390.52 -	390.52	98.70	03/2019 -	04/2019	1(O) -	0/0
233	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU , G	05/2016	4,497.00 -	4,497.00	24.07	12/2018 -	12/2018	0(O) -	0/2
234	AUGMENTATION OF CTMPL - [N16000286]IOCL,TAMIL NADU , Central Sector Projects	12/2016	228.00 -	228.00	-	06/2020 -	06/2020	0(O) -	0/0
235	SONAMURA GGS AND PIPELINE PROJECT (PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A - [N16000246]ONGC,TRIPURA , G	05/2016	215.38 -	215.38	162.34	06/2017 01/2018	01/2018	7(O) 0(R)	0/0
236	AURAIYA PHULPUR PIPELINE PROJECT - [N16000231]GAIL,UTTAR PRADESH , G	07/2015	1,427.94 -	1,427.94	434.76	12/2018 -	12/2018	0(O) -	12/20
237	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]GAIL,UTTAR PRADESH , Central Sector Projects	04/2017	287.49 -	287.49	14.70	04/2022 -	04/2022	0(O) -	0/0
238	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND , Central Sector Projects	02/2017	160.10 -	160.10	20.22	02/2020 -	02/2020	0(O) -	0/0
239	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL , G	03/2014	3,076.00 4,190.00	4,190.00	2,125.22	09/2017 06/2018	06/2018	9(O) 0(R)	6/7
240	NEW 250 TMTA LPG PLANT AT PANAGARH - [N16000222]HPCL,WEST BENGAL , G	08/2014	190.45 -	190.45	130.15	09/2017 03/2018	03/2018	6(O) 0(R)	0/0
241	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL,WEST BENGAL , G	03/2015	694.00 -	694.00	197.10	10/2018 -	10/2018	0(O) -	0/0
242	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL,WEST BENGAL , G	04/2016	1,021.00 -	1,021.00	6.35	12/2020 -	12/2020	0(O) -	0/0
243	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]GAIL,WEST BENGAL , G	03/2017	1,828.00 -	1,828.00	.93	12/2020 -	12/2020	0(O) -	0/24
	Total		1,92,892.26 -	1,94,226.73	53,688.09				389/899
	<u>POWER</u>								
244	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]PGCIL,ANDHRA PRADESH , G	03/2015	550.06 -	550.06	469.73	03/2018 -	09/2017	-	3/3
245	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]PGCIL,ANDHRA PRADESH , G	01/2016	207.88 -	207.88	90.85	07/2018 -	07/2018	0(O) -	0/0
246	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH , G	09/2003	6,285.33 -	18,559.49	9,518.76	09/2010 -	-	-	0/0
247	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH , G	12/2004	2,496.90 6,179.96	6,179.96	5,990.92	12/2009 03/2018	03/2018	99(O) 0(R)	18/30

Detail of ongoing Projects Costing Rs150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
248	PARE HYDRO ELECTRIC PROJECT - [N18000045]NNEPCO,ARUNACHAL PRADESH , G	12/2008	573.99 1,337.76	1,337.76	1,508.72	08/2013 03/2018	03/2018	55(O) 0(R)	32/38
249	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM , G	01/2008	4,375.35 8,149.00	8,149.00	6,815.00	09/2011 06/2017	03/2018	78(O) 9(R)	31/37
250	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR , G	02/2005	8,692.97 15,095.67	15,095.67	13,727.00	01/2011 05/2018	03/2019	98(O) 10(R)	26/47
251	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR , G	01/2007	5,353.00 7,998.00	7,998.00	6,838.73	05/2014 09/2017	02/2019	57(O) 17(R)	2/18
252	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR , Joint Venture	01/2013	12,964.60 -	13,731.26	10,084.21	01/2018 -	12/2018	11(O) -	27/31
253	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN,BIHAR , G	05/2015	436.68 -	602.44	473.75	12/2016 -	12/2017	12(O) -	9/16
254	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]PGCIL,BIHAR , G	04/2016	790.13 -	790.30	289.21	06/2019 -	06/2019	0(O) -	0/0
255	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH , G	12/2011	1,746.65 2,228.71	2,228.71	1,963.69	08/2014 12/2017	12/2017	40(O) 0(R)	7/11
256	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH , G	12/2012	11,846.00 -	11,846.00	8,673.00	06/2017 12/2017	12/2018	18(O) 12(R)	33/40
257	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI , G	03/2015	1,394.52 -	1,394.52	24.47	05/2017 06/2019	06/2019	25(O) 0(R)	4/9
258	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL,DELHI , G	05/2015	780.33 -	780.33	32.82	10/2018 -	10/2018	0(O) -	0/0
259	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) - [N18000207]PGCIL,GUJARAT , G	01/2016	244.19 -	244.19	116.50	07/2018 -	10/2017	-9(O) -	0/0
260	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]PGCIL,GUJARAT , G	07/2016	300.94 -	300.94	32.90	12/2018 -	12/2018	0(O) -	0/0
261	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]SJVN,GUJARAT , G	11/2016	330.00 -	330.00	185.90	11/2017 -	11/2017	0(O) -	1/4
262	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT , Central Sector Projects	05/2017	175.64 -	175.64	4.99	09/2018 -	09/2018	0(O) -	0/0
263	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH , G	09/2002	3,919.59 -	8,398.75	6,529.67	09/2009 -	12/2018	111(O) -	2/3
264	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR , G	01/2009	3,642.04 -	5,882.01	5,073.99	01/2016 -	02/2018	25(O) -	6/6
265	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR , G	10/2014	8,112.12 -	8,112.12	881.41	04/2020 12/2017	06/2023	38(O) 66(R)	0/0
266	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI- LEH PROJECT - [N18000215]PGCIL,JAMMU AND KASHMIR , G	01/2014	1,788.41 -	2,333.71	1,204.26	09/2017 -	09/2018	12(O) -	0/0
267	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND , G	02/2014	14,366.58 -	14,366.58	5,674.00	02/2019 02/2020	09/2020	19(O) 7(R)	18/20
268	BOKARO THERMAL POWER STATION-A - [N18000199]DVC,JHARKHAND , G	08/2006	2,313.00 4,138.41	4,366.64	3,484.00	12/2011 03/2016	02/2017	-	14/14

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
269	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND , G	10/2004	4,237.96 4,552.00	4,552.00	2,229.09	10/2017 12/2016	10/2017	0(O) 10(R)	0/0
270	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA , G	01/2012	15,166.19 -	15,166.19	14,506.00	01/2017 07/2017	12/2017	11(O) 5(R)	47/48
271	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA , Central Sector Projects	05/2017	445.89 -	445.89	-	02/2019 -	02/2019	0(O) -	0/0
272	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH , G	03/2013	11,638.55 -	11,638.55	8,244.00	09/2017 03/2018	09/2018	12(O) 6(R)	32/41
273	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC,MADHYA PRADESH , G	03/2015	9,870.51 -	9,870.51	3,537.00	09/2019 -	09/2019	0(O) -	22/22
274	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH , G	01/2016	305.04 -	305.04	161.56	03/2017 10/2017	12/2017	9(O) 2(R)	0/0
275	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]PGCIL,MADHYA PRADESH , G	04/2016	287.99 -	287.99	75.18	06/2018 -	06/2018	0(O) -	0/0
276	AMELIA COAL MINE - [N18000252]THDCIL,MADHYA PRADESH , Central Sector Projects	01/2017	2,104.21 -	2,104.21	40.37	09/2020 -	09/2020	0(O) -	9/16
277	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V - [N18000256]PGCIL,MADHYA PRADESH , Central Sector Projects	02/2015	1,750.00 -	1,750.00	458.00	06/2018 -	06/2018	0(O) -	0/0
278	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA , G	12/2007	477.69 738.48	738.48	649.35	09/2010 12/2017	03/2018	90(O) 3(R)	4/8
279	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA , G	03/2012	7,921.47 -	7,921.47	5,302.00	09/2016 03/2017	03/2017	-	41/41
280	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA , G	03/2012	9,395.18 -	9,395.18	8,128.00	11/2016 12/2017	12/2018	25(O) 12(R)	34/36
281	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-B - [N18000255]PGCIL,MAHARASHTRA , Central Sector Projects	04/2015	2,225.00 2,225.00	2,225.00	869.00	01/2018 -	01/2018	0(O) -	0/0
282	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM , G	07/1998	368.72 1,329.43	1,329.43	1,288.82	07/2006 11/2017	11/2017	136(O) 0(R)	6/13
283	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE , G	10/2008	4,824.12 5,071.94	5,071.94	4,484.38	10/2012 02/2018	02/2018	64(O) 0(R)	8/11
284	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE , G	02/2009	11,130.19 13,762.80	13,762.80	12,558.71	08/2013 12/2017	12/2017	52(O) 0(R)	22/26
285	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE , G	02/2010	2,144.00 2,932.88	2,932.88	2,566.17	12/2012 02/2018	02/2018	62(O) 0(R)	16/23
286	SYSTEM STRENGTHENING XII OF SR - [N18000085]PGCIL,MULTI STATE , G	02/2010	232.34 -	245.00	238.62	06/2012 -	12/2017	66(O) -	1/4
287	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE , G	07/2010	1,272.80 1,731.10	1,731.10	1,417.01	11/2012 12/2017	12/2017	61(O) 0(R)	10/13
288	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE , G	10/2011	487.49 639.46	639.46	485.42	06/2014 03/2018	09/2018	51(O) 6(R)	10/12
289	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE , G	12/2011	297.33 346.79	426.29	361.27	08/2014 12/2017	12/2017	40(O) 0(R)	8/10

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
290	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE , G	03/2012	198.63 -	198.63	135.62	09/2014 09/2017	01/2018	40(O) 4(R)	0/0
291	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE , G	11/2011	723.63 882.13	882.13	721.43	11/2014 06/2017	12/2017	37(O) 6(R)	7/10
292	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE , G	03/2013	514.20 703.10	703.10	581.72	06/2015 12/2017	03/2018	33(O) 3(R)	7/10
293	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE , G	03/2013	2,514.88 -	2,514.88	2,011.63	12/2015 12/2017	03/2018	27(O) 3(R)	15/18
294	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE , G	10/2013	1,364.52 1,891.41	1,891.41	1,166.14	04/2016 09/2017	03/2018	23(O) 6(R)	8/12
295	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE , G	01/2014	374.63 -	374.63	116.52	04/2016 12/2017	12/2017	20(O) 0(R)	0/0
296	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE , G	02/2014	539.82 -	539.82	388.72	06/2016 02/2018	02/2018	20(O) 0(R)	9/11
297	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL,MULTI STATE , G	02/2014	908.08 969.97	969.97	722.47	06/2016 02/2018	11/2017	17(O) -3(R)	16/18
298	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE , G	05/2014	829.98 -	829.98	410.67	08/2016 10/2017	12/2017	16(O) 2(R)	2/4
299	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE , G	05/2014	522.29 550.18	550.18	366.29	11/2016 11/2017	03/2018	16(O) 4(R)	7/12
300	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE , G	03/2014	155.57 206.42	206.42	134.03	03/2016 07/2017	12/2017	21(O) 5(R)	3/6
301	TRANSMISSION SYSTEM STRENGTHENING IN WR- NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE , G	06/2014	5,151.37 -	5,151.37	1,622.82	03/2018 -	06/2018	3(O) -	8/12
302	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE , G	08/2014	288.49 -	376.09	226.73	02/2017 06/2017	03/2018	13(O) 9(R)	7/12
303	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE , G	02/2014	196.58 225.28	225.28	133.69	02/2016 08/2017	12/2017	22(O) 4(R)	12/17
304	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]PGCIL,MULTI STATE , G	12/2014	6,517.36 -	6,517.36	3,477.53	04/2018 -	04/2018	0(O) -	3/12
305	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]PGCIL,MULTI STATE , G	01/2015	268.80 340.88	340.88	161.96	03/2018 -	03/2018	0(O) -	0/3
306	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE , G	01/2015	871.62 -	871.62	146.64	10/2017 10/2017	06/2018	8(O) 8(R)	0/5
307	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE , G	01/2015	203.28 260.03	260.03	165.86	07/2017 -	12/2018	17(O) -	3/5
308	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE , G	03/2015	197.40 -	197.40	48.84	03/2018 -	03/2018	0(O) -	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
309	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE , G	03/2015	1,071.24 -	1,071.24	465.53	09/2017 -	04/2018	7(O) -	0/0
310	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE , G	04/2015	3,705.61 -	3,705.61	2,144.69	04/2018 -	07/2018	3(O) -	4/9
311	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]PGCIL,MULTI STATE , G	04/2015	1,479.30 -	1,479.30	726.01	04/2017 03/2018	03/2018	11(O) 0(R)	2/8
312	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL,MULTI STATE , G	07/2015	2,247.37 -	2,247.37	688.65	07/2018 -	07/2018	0(O) -	0/0
313	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL,MULTI STATE , G	01/2016	1,455.47 -	1,455.47	557.91	07/2018 -	07/2018	0(O) -	0/0
314	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE , G	03/2016	808.63 -	808.63	207.14	01/2018 -	03/2019	14(O) -	0/0
315	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]PGCIL,MULTI STATE , G	05/2016	766.21 -	766.21	59.23	11/2018 -	11/2018	0(O) -	0/0
316	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE , G	05/2016	3,519.59 -	3,519.59	446.63	05/2019 -	05/2019	0(O) -	0/0
317	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE , G	05/2016	14,733.37 -	14,733.37	698.45	11/2019 -	11/2019	0(O) -	0/0
318	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I - [N18000220]PGCIL,MULTI STATE , G	04/2016	810.48 -	810.48	355.87	12/2018 -	12/2018	0(O) -	0/0
319	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]PGCIL,MULTI STATE , G	05/2016	167.01 -	167.01	40.22	11/2018 -	11/2018	0(O) -	0/0
320	WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]PGCIL,MULTI STATE , G	07/2016	150.99 -	150.99	29.37	07/2018 -	07/2018	0(O) -	0/0
321	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]PGCIL,MULTI STATE , G	07/2016	333.17 -	333.17	148.98	03/2019 -	03/2019	0(O) -	0/0
322	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]PGCIL,MULTI STATE , G	08/2016	431.89 -	431.89	.62	02/2019 -	02/2019	0(O) -	0/0
323	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232]PGCIL,MULTI STATE , G	08/2016	177.52 -	177.52	10.95	02/2019 -	02/2019	0(O) -	0/0
324	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE , G	09/2016	562.25 -	562.25	18.56	03/2019 -	03/2019	0(O) -	0/0
325	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]PGCIL,MULTI STATE , G	03/2017	251.60 -	251.60	-	06/2019 -	06/2019	0(O) -	0/0
326	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION - [N18000237]PGCIL,MULTI STATE , G	10/2016	167.75 -	167.75	1.16	04/2019 -	04/2019	0(O) -	0/0
327	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE , G	03/2017	283.72 -	283.72	7.71	11/2019 -	11/2019	0(O) -	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
328	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE , G	10/2016	408.46 -	408.46	41.84	01/2019 -	01/2019	0(O) -	0/0
329	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE , G	10/2016	608.24 -	608.24	6.28	04/2019 -	04/2019	0(O) -	0/0
330	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]PGCIL,MULTI STATE , G	02/2017	195.05 -	195.05	-	02/2020 -	02/2020	0(O) -	0/0
331	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE , G	02/2017	322.30 -	322.30	15.11	02/2019 -	02/2019	0(O) -	0/0
332	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODHISHA - [N18000243]PGCIL,MULTI STATE , G	03/2017	162.31 -	162.31	.62	03/2019 -	03/2019	0(O) -	0/0
333	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE , G	02/2017	235.53 -	235.53	7.29	06/2019 -	06/2019	0(O) -	0/0
334	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE , G	03/2017	379.95 -	379.95	19.67	12/2019 -	12/2019	0(O) -	0/0
335	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]PGCIL,MULTI STATE , G	02/2017	204.12 -	204.12	7.45	09/2019 -	09/2019	0(O) -	0/0
336	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL,MULTI STATE , G	02/2017	5,070.13 -	5,070.13	240.02	04/2020 -	04/2020	0(O) -	0/0
337	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE , G	03/2017	337.75 -	337.75	-	06/2019 -	06/2019	0(O) -	0/0
338	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE , G	12/2014	4,754.42 -	4,754.42	399.63	12/2018 -	12/2019	12(O) -	0/0
339	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE , G	12/2014	5,111.33 -	5,111.33	363.42	12/2018 -	12/2019	12(O) -	0/0
340	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]PGCIL,MULTI STATE , Central Sector Projects	03/2015	955.00 1,161.00	1,364.00	1,083.00	12/2015 -	03/2018	27(O) -	0/0
341	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A) - [N18000254]PGCIL,MULTI STATE , Central Sector Projects	04/2015	2,525.00 -	2,525.00	1,370.00	11/2017 -	01/2018	2(O) -	0/0
342	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE , Central Sector Projects	12/2015	3,654.00 -	3,654.00	951.00	04/2019 -	04/2019	0(O) -	0/0
343	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE , Central Sector Projects	03/2017	3,500.00 3,500.00	3,500.00	55.00	07/2020 -	07/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
344	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE , Central Sector Projects	08/2017	1,931.39 -	1,931.39	6.91	02/2020 -	02/2020	0(O) -	0/0
345	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA , G	02/2014	12,532.44 -	12,532.44	6,433.00	08/2018 -	11/2018	3(O) -	25/31
346	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA , G	04/2016	844.64 -	844.64	126.12	04/2019 -	04/2019	0(O) -	0/0
347	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN , G	07/2015	307.18 -	307.18	174.58	11/2017 -	06/2018	7(O) -	0/0
348	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203]NHPC,RAJASTHAN , G	02/2015	302.49 302.00	302.49	270.77	02/2016 -	-	-	1/1
349	TRAMMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL,RAJASTHAN , G	07/2016	1,429.38 -	1,429.38	113.56	01/2019 -	01/2019	0(O) -	0/0
350	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU , G	05/2005	1,779.29 2,187.32	2,187.32	1,958.79	11/2008 09/2018	09/2018	118(O) 0(R)	20/22
351	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU , G	09/2011	1,940.13 2,702.65	2,702.65	2,338.48	09/2014 06/2017	12/2017	39(O) 6(R)	11/13
352	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]PGCIL,TAMIL NADU , G	01/2016	162.11 -	162.11	115.28	05/2018 -	12/2017	-5(O) -	0/0
353	50 MW SOLAR POWER PROJECT - [N18000251]NHPC,TAMIL NADU , G	09/2017	287.48 -	287.48	28.25	03/2018 -	03/2018	0(O) -	0/0
354	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU , Central Sector Projects	05/2017	186.17 -	186.17	7.74	07/2019 -	07/2019	0(O) -	0/0
355	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA , G	01/2016	10,598.98 -	10,598.98	1,043.00	07/2020 -	07/2020	0(O) -	13/18
356	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA , G	07/2009	421.01 1,078.31	1,078.31	963.23	07/2013 -	-	-	26/26
357	NORTH EASTERN REGION STRENGTHENING SCHEME IV - [N18000216]PGCIL,TRIPURA , G	05/2016	409.19 -	409.19	55.00	05/2018 -	05/2018	0(O) -	0/0
358	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH , G	07/2013	3,363.12 -	3,363.12	2,244.00	12/2016 -	-	-	28/28
359	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH , G	09/2014	9,188.98 -	9,188.98	3,231.00	03/2019 -	06/2019	3(O) -	19/27
360	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH , G	05/2011	195.42 294.60	294.60	133.33	02/2014 02/2018	12/2018	58(O) 10(R)	3/5
361	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH , Joint Venture	04/2012	9,750.89 -	9,750.89	6,957.91	12/2016 -	02/2019	26(O) -	29/34
362	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND , G	07/2006	1,657.00 2,978.86	3,939.11	2,394.81	02/2016 09/2019	12/2020	58(O) 15(R)	16/26
363	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND , G	11/2006	2,978.48 -	3,846.30	3,321.00	03/2013 06/2019	03/2020	84(O) 9(R)	3/15
364	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND , G	08/2008	2,491.58 -	2,491.58	1,264.31	06/2013 -	11/2020	89(O) -	8/11

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
365	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND , G	07/2012	1,527.00 -	1,527.00	148.00	08/2017 -	08/2017	-	0/15
366	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL,WEST BENGAL , G	04/2010	4,404.57 5,135.01	5,135.01	3,464.70	01/2015 03/2018	03/2018	38(O) 0(R)	14/16
367	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL , G	09/2014	1,381.84 -	1,381.84	294.00	09/2019 -	03/2021	18(O) -	5/7
368	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]DVC,WEST BENGAL , G	04/2007	4,122.00 8,781.30	9,142.58	8,300.00	02/2011 -	03/2016	-	26/26
369	EASTERN REGION STRENGTHENNING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL , G	04/2016	454.11 -	454.11	81.02	04/2018 -	04/2018	0(O) -	0/0
	Total		3,38,804.33 -	3,97,533.16	2,26,664.54				863/1156
	<u>HEAVY INDUSTRY</u>								
370	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE , G	04/2011	1,718.00 -	3,827.30	2,289.00	09/2011 -	12/2017	75(O) -	0/0
	Total		1,718.00 -	3,827.30	2,289.00				0/0
	<u>HEALTH AND FAMILY WELFARE</u>								
371	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH , Central Sector Projects	08/2017	272.19 -	272.19	5.45	03/2019 -	03/2019	0(O) -	0/0
372	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM , G	07/2012	175.57 -	175.57	113.50	12/2014 -	-	-	0/0
373	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI , G	02/2013	414.11 -	414.11	141.00	11/2013 -	-	-	0/0
374	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK - [N21000004]HSCC,DELHI , G	09/2013	444.70 -	444.70	326.30	12/2015 -	-	-	0/0
375	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005]HSCC,DELHI , G	11/2013	196.70 -	209.00	170.00	01/2016 -	-	-	0/0
376	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI , G	12/2013	204.44 -	204.44	137.00	05/2017 -	06/2018	13(O) -	0/2
377	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI , G	08/2014	293.65 -	293.65	207.00	05/2017 -	09/2018	16(O) -	0/5
378	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA , G	09/2014	505.58 -	505.58	238.00	03/2018 -	03/2018	0(O) -	0/2
379	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA - [N21000014]HSCC,HARYANA , G	07/2016	312.99 -	312.99	128.00	08/2018 -	08/2018	0(O) -	0/1
380	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA , Central Sector Projects	08/2017	274.19 -	274.19	5.48	03/2019 -	03/2019	0(O) -	0/0
381	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA , G	10/2016	363.99 -	363.99	14.00	05/2018 08/2019	08/2019	15(O) 0(R)	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
382	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB , G	07/2016	152.95 -	152.95	34.00	02/2018 -	08/2018	6(O) -	0/1
383	AIIMS-RAE BARELI-HOUSING - [N21000006]HSCC,UTTAR PRADESH , G	10/2013	159.50 -	159.50	158.65	11/2013 06/2017	06/2017	-	0/8
384	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL , G	12/2014	168.90 -	168.90	108.00	05/2017 -	03/2018	10(O) -	0/3
385	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL , G	08/2016	244.00 -	244.00	72.00	09/2018 -	09/2018	0(O) -	0/0
386	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL , Central Sector Projects	08/2017	355.15 -	355.15	7.10	03/2019 -	03/2019	0(O) -	0/0
	Total		4,538.61 -	4,550.91	1,865.48				0/22
	<u>RAILWAYS</u>								
387	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH , G	03/1996	155.74 164.36	966.98	874.72	02/2009 -	12/2017	106(O) -	0/0
388	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH , G	12/2001	330.00 -	2,125.18	14.17	-	03/2021	-	0/0
389	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH , G	04/2003	136.62 -	376.00	1,011.85	12/2007 03/2010	-	-	0/0
390	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH , G	07/2006	743.00 -	1,825.00	1,410.14	03/2008 06/2008	03/2020	144(O) 141(R)	0/0
391	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH , G	04/2011	283.54 -	759.41	.51	-	-	-	0/0
392	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH , G	04/2013	829.00 -	829.00	.48	-	-	-	0/1
393	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH , G	04/2011	1,313.48 -	1,313.48	8.06	-	-	-	0/1
394	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH , G	03/2012	1,503.71 -	1,503.71	497.81	-	03/2020	-	0/0
395	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH , G	04/2015	3,873.07 -	3,873.07	-	-	-	-	0/0
396	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH , G	04/2016	4,000.00 -	3,631.00	-	-	-	-	0/0
397	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH , G	04/2015	3,246.26 -	3,548.67	37.25	-	-	-	0/0
398	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH , G	04/2015	2,499.71 -	2,499.71	25.30	03/2021 -	03/2022	12(O) -	0/0
399	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH , G	01/2013	387.70 -	387.70	351.28	03/2018 -	03/2018	0(O) -	0/0
400	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH , G	08/2016	234.50 -	234.50	.39	03/2019 -	03/2019	0(O) -	0/0
401	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM , G	09/1997	1,500.00 -	5,450.00	4,837.30	04/2008 12/2011	06/2018	122(O) 78(R)	0/0
402	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM , G	09/2006	200.00 -	780.00	427.71	-	03/2019	-	0/0
403	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM , G	04/1998	227.90 -	509.00	412.40	12/2012 -	05/2016	-	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
404	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM , G	04/1996	1,676.31 -	7,300.00	7,082.91	03/2009 -	03/2018	108(O) -	0/0
405	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM , G	04/2011	312.12 -	535.00	495.86	- -	03/2019	- -	0/0
406	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM , G	04/2012	246.07 -	398.93	102.71	- -	03/2019	- -	0/0
407	LUMDING-DIBRUGARH (628 KM) INCL. LINK BRANCH LINES OF HAIBARGAON-MAIRABARI (89 KM) - [N22000385]NFR,ASSAM , G	04/2003	971.22 -	966.27	834.11	- -	12/2009	-	0/0
408	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS - [N22000386]NFR,ASSAM , G	04/2003	4,300.00 -	4,520.00	4,422.02	- -	08/2015	-	0/0
409	NEW GUWAHATI-DIGARU-PATCH DOUBLING - [N22000387]NFR,ASSAM , G	04/2007	180.09 -	180.00	157.12	- -	05/2011	-	0/0
410	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM , G	04/2015	2,232.32 -	2,232.00	63.61	- -	03/2021	- -	0/0
411	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM , G	04/2015	870.96 -	871.00	21.00	- -	03/2021	- -	0/0
412	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR , G	04/1997	501.69 335.77	1,043.56	876.49	03/2012 -	-	-	0/0
413	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR , G	09/2001	492.98 -	1,320.00	919.93	12/2010 -	-	-	0/0
414	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR , G	04/1997	162.87 -	541.00	183.72	- -	-	-	0/0
415	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR , G	04/2003	528.65 -	324.66	330.82	- -	-	-	0/0
416	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR , G	04/2002	322.95 -	341.41	320.39	03/2012 -	-	-	0/0
417	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR , G	04/2001	406.92 -	339.00	200.00	- -	-	-	0/0
418	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR , G	04/2003	218.19 -	412.05	356.65	- -	03/2018	- -	0/0
419	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR , G	04/1996	332.92 283.95	477.88	495.40	03/2012 -	-	-	0/0
420	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR , G	09/2006	300.00 -	2,135.00	921.06	- -	03/2020	- -	0/0
421	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR , G	04/2008	282.92 -	360.00	3.13	- -	-	-	0/0
422	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR , G	04/2008	490.80 -	490.80	.39	- -	-	-	0/0
423	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR , G	04/2008	620.57 -	620.57	-	- -	-	-	0/0
424	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR , G	04/2008	445.25 -	445.25	-	- -	-	-	0/0
425	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR , G	04/2008	326.20 -	326.20	1.68	- -	-	-	0/0
426	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR , G	04/1999	175.69 -	325.00	253.10	- -	-	-	0/0
427	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR , G	04/2006	285.07 -	378.56	111.71	- -	-	-	0/0
428	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR , G	04/2005	205.00 -	205.00	5.21	- -	-	-	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
429	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR , G	04/2006	211.00 -	926.09	4.41	- -	-	-	0/0
430	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR , G	04/2008	678.62 -	2,393.23	17.17	- -	-	-	0/0
431	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR , G	04/2008	228.05 -	228.05	1.52	- -	-	-	0/0
432	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR , G	04/2008	304.41 -	304.41	.19	- -	-	-	0/0
433	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR , G	04/2008	192.56 -	192.56	.38	- -	-	-	0/0
434	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR , G	04/2008	281.30 -	281.30	.58	- -	-	-	0/0
435	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR , G	04/2004	372.14 -	355.81	283.44	- -	-	-	0/0
436	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR , G	04/2009	470.00 -	470.00	40.00	- -	-	-	0/0
437	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR , G	04/2013	213.01 -	367.17	13.00	- -	-	-	0/0
438	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR , G	05/2015	380.00 -	380.00	-	- -	-	-	0/0
439	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR , G	12/2015	1,200.20 -	1,200.20	-	12/2020 -	12/2020	0(O) -	0/1
440	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR , G	12/2015	1,491.47 -	1,491.47	-	12/2020 -	12/2020	0(O) -	1/1
441	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR , G	01/1991	332.15 -	559.91	538.21	07/2014 -	-	-	0/0
442	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH , G	04/1995	304.00 -	1,195.00	328.04	12/2012 -	-	-	0/0
443	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH , G	09/2006	324.90 -	516.40	710.67	03/2010 -	12/2017	93(O) -	0/3
444	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH , G	12/2012	826.57 -	1,160.83	452.03	- -	03/2020	-	0/1
445	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH , G	03/2007	758.09 -	758.09	826.51	03/2020 -	03/2020	0(O) -	0/0
446	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH , G	05/2014	207.00 -	207.00	142.00	03/2018 -	03/2018	0(O) -	0/0
447	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI , G	04/1999	156.65 -	197.17	56.10	- -	-	-	0/0
448	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI , G	04/2012	295.68 -	295.68	1.20	- -	-	-	0/0
449	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT , G	04/2008	394.14 -	385.60	27.69	03/2013 -	03/2020	84(O) -	0/0
450	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT , G	04/2008	1,389.62 -	1,389.62	1,513.78	03/2014 -	12/2017	45(O) -	0/0
451	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT , G	04/2008	318.24 -	321.62	37.15	03/2012 -	03/2019	84(O) -	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
452	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT , G	04/2006	117.36 196.95	203.00	202.29	03/2011 -	-	-	0/0
453	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT , G	04/2012	567.18 -	975.62	2,326.34	- -	03/2020	-	0/0
454	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT , G	04/2012	376.59 -	644.38	28.31	- -	12/2020	-	0/0
455	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT , G	04/2011	439.88 -	845.68	.78	- -	-	-	0/0
456	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT , G	04/1994	320.66 -	399.63	-	- -	03/2019	-	0/0
457	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT , G	04/2013	1,266.89 -	1,548.66	376.11	- -	12/2020	-	0/0
458	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT , G	04/2011	446.00 -	1,037.15	590.60	- -	03/2019	-	0/0
459	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT , G	04/2010	279.40 -	355.00	323.64	- -	-	-	0/0
460	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT , G	04/2015	1,002.39 -	1,002.39	-	- -	03/2021	-	0/0
461	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT , G	10/2013	343.00 -	343.00	240.72	03/2019 -	03/2019	0(O) -	0/0
462	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA , G	01/2004	238.56 -	740.00	722.65	03/2012 -	-	-	0/0
463	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA , G	04/2012	287.00 -	625.00	4.38	- -	-	-	0/0
464	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA , G	04/2013	400.00 -	400.00	-	- -	-	-	0/0
465	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA , G	05/2015	400.00 -	400.00	-	- -	-	-	0/0
466	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA , G	12/2015	346.32 -	300.00	206.47	03/2019 -	03/2019	0(O) -	0/0
467	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH , G	04/2008	1,046.88 -	4,500.00	108.06	- -	-	-	0/0
468	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR , G	03/1995	2,500.00 19,565.00	27,946.00	15,803.00	11/2002 -	12/2018	193(O) -	0/0
469	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND , G	04/1995	900.05 -	1,125.89	980.99	12/2011 12/2010	03/2020	99(O) 111(R)	0/0
470	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND , G	04/1997	194.07 -	491.33	548.77	06/2004 -	-	-	0/0
471	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND , G	04/2002	459.91 -	459.91	221.54	- -	-	-	0/0
472	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]RVNL,JHARKHAND , G	03/1997	261.70 -	388.00	795.83	02/2006 -	12/2019	166(O) -	0/1
473	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND , G	04/2008	167.73 -	167.73	207.11	03/2012 -	-	-	0/0
474	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND , G	04/2010	309.44 -	583.00	402.65	12/2015 -	-	-	0/0
475	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND , G	04/2012	258.20 -	365.00	98.37	- -	12/2017	-	0/0
476	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND , G	04/2012	148.77 -	209.00	105.32	12/2016 -	-	-	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
477	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND , G	03/2016	1,724.20 -	1,724.20	126.44	03/2021 -	03/2021	0(O) -	0/0
478	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA , G	04/1997	227.00 -	2,135.00	133.87	- -	-	-	0/0
479	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA , G	02/1998	242.42 369.70	1,542.41	927.68	- 05/2009	-	-	0/1
480	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA , G	04/1996	138.00 1,382.78	1,382.78	6.12	- -	-	-	0/0
481	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA , G	04/2007	482.00 -	874.57	989.29	03/2013 -	-	-	0/0
482	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA , G	04/2011	913.00 -	1,801.01	2.56	- -	-	-	0/0
483	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA , G	04/2007	179.65 -	1,350.91	782.44	- -	-	-	0/1
484	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA , G	04/2010	377.93 986.30	986.30	271.00	- -	-	-	0/1
485	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA , G	04/2013	558.00 692.43	692.43	-	- -	-	-	0/0
486	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA , G	04/2011	562.74 -	832.47	.94	- -	-	-	0/0
487	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA , G	04/2011	341.05 -	348.85	.35	- -	-	-	0/0
488	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA , G	04/2010	2,127.00 -	2,127.00	478.01	- -	03/2019	-	0/1
489	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA , G	04/2011	146.75 -	167.50	.34	- -	-	-	0/0
490	GADAG-WADI NL - [N22000299]SWR,KARNATAKA , G	04/2013	1,117.00 1,922.00	1,922.00	3.60	- -	-	-	0/0
491	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA , G	04/2013	327.25 367.77	367.77	-	- -	-	-	0/0
492	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA , G	04/2012	285.57 279.54	279.54	3.16	01/1999 -	-	-	0/0
493	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA , G	03/2015	1,900.00 1,141.00	1,141.00	448.65	- 03/2020	-	-	0/5
494	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA , G	03/2015	960.00 578.00	578.00	306.27	- 11/2015	03/2020	- 52(R)	0/2
495	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA , G	10/1998	550.00 -	2,815.62	240.68	- -	01/2018	-	0/0
496	KUMBALAM-TURAVUR - [N22000191]SR,KERALA , G	04/2011	252.96 -	252.96	7.74	- -	-	-	0/0
497	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA , G	04/2006	191.72 -	342.85	360.22	- -	-	-	0/0
498	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA , G	04/2010	189.24 -	189.24	189.35	- -	12/2017	-	0/0
499	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA , G	02/2015	900.00 -	4,131.90	-	- -	-	-	0/0
500	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA , G	02/2015	1,000.00 -	1,000.00	-	- -	-	-	0/0
501	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH , G	04/2001	470.92 727.13	2,713.09	632.05	- -	03/2021	-	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
502	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH , G	04/2005	383.79 -	1,101.16	194.91	- -	-	-	0/0
503	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH , G	09/2007	687.20 -	950.00	679.56	03/2010 -	03/2018	96(O) -	0/0
504	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH , G	04/2008	603.04 -	1,030.29	628.11	03/2012 -	-	-	0/0
505	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH , G	12/2015	1,762.94 -	1,762.94	-	12/2020 -	12/2020	0(O) -	1/1
506	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH , G	04/2011	1,485.65 -	1,485.85	686.19	12/2020 -	12/2020	0(O) -	0/0
507	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH , G	06/2016	2,478.23 -	2,478.23	-	03/2022 -	03/2022	0(O) -	0/1
508	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH , G	08/2016	582.13 -	582.13	-	03/2020 -	03/2020	0(O) -	0/1
509	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH , G	12/2015	174.00 -	174.00	94.20	03/2019 -	03/2019	0(O) -	0/0
510	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA , G	06/1994	663.01 668.34	858.97	696.87	06/1999 -	-	-	0/0
511	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA , G	03/1996	495.44 1,781.98	1,781.98	667.06	03/2004 -	03/2020	192(O) -	0/0
512	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]CR,MAHARASHTRA , G	02/1997	514.68 -	2,271.50	812.01	- -	-	-	0/0
513	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA , G	04/2008	5,300.00 -	7,986.04	2,423.55	03/2014 -	03/2019	60(O) -	0/0
514	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA , G	04/2012	714.10 -	714.10	65.20	04/2016 -	-	-	0/0
515	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA , G	04/2008	499.30 2,491.43	3,168.29	708.27	- -	03/2023	-	0/0
516	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA , G	04/2011	277.70 792.89	792.89	205.77	- -	03/2021	-	0/0
517	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA , G	04/2011	184.06 -	199.12	142.22	- -	-	-	0/0
518	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA , G	04/2012	297.85 540.02	540.02	119.78	- -	03/2022	-	0/0
519	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA , G	02/2016	9,968.00 -	9,968.00	-	- -	-	-	0/0
520	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA , G	02/2016	2,425.00 -	2,425.00	-	- -	-	-	0/0
521	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA , G	02/2016	2,750.00 -	2,750.00	-	- -	-	-	0/0
522	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA , G	02/2015	630.00 1,272.19	1,272.19	53.59	- -	03/2022	-	0/0
523	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA , G	02/2015	2,326.00 2,449.91	2,449.91	12.78	- -	03/2023	-	0/0
524	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA , G	02/2015	4,670.00 3,627.00	3,627.47	-	- -	-	-	0/0
525	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA , G	02/2016	1,876.00 -	2,081.27	-	- -	-	-	0/0
526	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA , G	02/2016	854.00 -	1,035.16	-	- -	-	-	0/0
527	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA , G	02/2016	912.00 637.95	637.95	.36	- -	03/2022	-	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
528	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA , G	03/2009	1,514.45 -	1,514.45	-	03/2020 -	03/2020	0(O) -	0/0
529	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA , G	04/2015	723.78 -	723.78	.22	12/2025 -	12/2025	0(O) -	0/0
530	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA , G	09/2016	1,273.00 1,908.00	1,908.00	-	12/2021 -	12/2021	0(O) -	0/0
531	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA , G	10/2013	305.00 -	305.00	218.41	03/2019 -	03/2019	0(O) -	0/0
532	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR , G	04/2003	727.56 -	9,658.00	5,464.91	03/2011 -	03/2020	108(O) -	0/0
533	NEW BG LINE FROM BYRNHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA , G	04/2010	4,083.02 -	6,000.00	252.01	- -	03/2021	- -	0/0
534	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM , G	04/2008	619.34 -	4,600.00	1,749.95	04/2014 -	03/2020	71(O) -	0/0
535	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE , G	04/1986	158.77 274.56	634.48	629.43	03/1994 -	-	-	0/0
536	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE , G	02/1996	240.00 -	579.37	537.02	- -	-	-	0/0
537	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE , G	02/1997	386.30 -	1,776.81	967.96	03/1998 -	12/2019	261(O) -	0/0
538	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE , G	03/1981	450.00 -	2,100.00	484.14	07/2012 -	-	-	0/0
539	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205]SCR,MULTI STATE , G	04/1997	218.24 236.41	525.00	544.20	- -	03/2019	-	0/0
540	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE , G	09/1998	247.66 -	6,093.31	972.82	05/2008 -	03/2023	178(O) -	0/4
541	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE , G	04/1999	744.71 744.71	1,126.79	761.70	- -	-	-	1/1
542	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE , G	03/2002	625.30 408.76	876.10	841.57	06/2007 -	-	-	0/0
543	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE , G	03/1998	280.00 -	1,122.00	834.61	- -	-	-	0/6
544	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE , G	04/2000	733.00 -	3,040.00	2,389.60	12/2008 -	03/2019	123(O) -	0/0
545	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE , G	04/1998	92.63 -	350.00	316.64	02/2011 -	-	-	0/0
546	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE , G	04/2000	607.09 -	973.33	613.71	12/2012 12/2012	-	-	0/0
547	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE , G	04/2005	230.03 -	718.54	275.20	- -	05/2019	-	0/0
548	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE , G	12/2006	170.00 -	465.00	440.72	03/2011 -	10/2011	-	0/0
549	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE , G	03/2007	243.78 -	268.78	96.78	- -	08/2017	-	0/0
550	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE , G	03/2013	295.00 -	477.31	97.07	- -	10/2018	-	0/0
551	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE , G	04/2007	1,347.26 -	1,347.26	270.58	- -	-	-	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
552	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE , G	04/2007	1,640.04 -	1,640.04	331.91	- -	03/2022	- -	0/0
553	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE , G	04/2011	2,082.75 -	2,562.27	179.56	- -	-	-	0/1
554	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE , G	04/2011	1,176.09 -	3,845.60	1.92	02/2020 -	12/2022	34(O) -	0/0
555	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE , G	04/2010	622.41 -	2,030.50	10.34	02/2019 -	12/2022	46(O) -	0/0
556	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE , G	04/2010	553.63 -	1,009.00	-	- -	-	-	0/0
557	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE , G	04/2008	415.67 -	549.75	14.62	- -	-	-	0/0
558	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE , G	04/2013	1,798.00 -	1,798.00	-	- -	03/2019	- -	0/0
559	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE , G	04/2008	523.52 -	2,350.00	2.27	- -	-	-	0/0
560	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]RVNL,MULTI STATE , G	04/2008	822.39 -	1,810.00	1,652.42	- -	03/2018	- -	0/1
561	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE , G	04/2007	270.14 -	346.15	253.87	- -	-	-	0/0
562	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE , G	04/2010	242.22 -	471.00	56.93	- -	-	-	0/0
563	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE , G	04/2010	241.52 -	394.28	148.33	- -	-	-	0/0
564	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE , G	04/2011	165.82 -	450.00	117.50	- -	03/2020	- -	0/0
565	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE , G	04/1999	523.17 -	1,871.00	1,071.96	- -	03/2018	- -	0/0
566	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE , G	04/2011	601.43 -	1,500.00	71.60	- -	-	-	0/0
567	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE , G	04/1987	406.99 -	319.58	141.88	- -	-	-	0/0
568	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE , G	04/2007	450.00 -	290.85	9.31	- -	-	-	0/0
569	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE , G	04/2010	172.03 -	260.60	6.42	- -	-	-	0/0
570	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE , G	04/2013	915.98 1,130.13	1,130.13	.30	- -	-	-	0/0
571	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE , G	04/2011	248.07 -	234.41	161.17	03/2015 -	-	-	0/0
572	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE , G	04/2011	288.35 -	238.36	51.31	- -	-	-	0/0
573	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE , G	04/2011	261.38 -	332.14	87.22	- -	-	-	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
574	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE , G	04/2001	923.52 -	923.52	227.50	- -	-	-	0/0
575	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE , G	04/2005	595.91 -	595.91	103.62	- -	-	-	0/0
576	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE , G	04/2010	174.56 -	160.97	56.25	- -	-	-	0/0
577	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE , G	04/2010	277.28 -	266.00	92.93	- -	-	-	0/0
578	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE , G	04/2010	296.44 -	198.88	15.83	- -	-	-	0/0
579	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE , G	04/2010	157.94 -	157.94	47.63	- -	11/2018	-	0/0
580	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE , G	04/2007	450.55 -	251.05	15.66	- -	-	-	0/0
581	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE , G	04/2010	365.17 -	365.67	1.37	- -	-	-	0/0
582	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE , G	04/2011	267.09 -	350.78	98.15	- -	-	-	0/0
583	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE , G	04/2011	193.44 -	186.64	150.28	- -	-	-	0/0
584	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE , G	04/2011	175.80 -	173.91	18.54	- -	-	-	0/0
585	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE , G	04/2011	299.60 -	269.60	1.11	03/2017 -	-	-	0/0
586	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE , G	04/2010	494.54 -	369.69	31.99	- -	-	-	0/0
587	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE , G	04/2000	297.47 -	153.02	52.01	- -	-	-	0/0
588	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE , G	04/2003	337.96 -	186.89	62.73	- -	-	-	0/0
589	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE , G	04/2009	493.96 -	681.68	135.79	- -	-	-	0/0
590	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE , G	04/2010	423.66 -	720.59	456.58	03/2017 -	-	-	0/0
591	SANTOSHPIUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE , G	04/2010	268.52 -	268.52	78.81	- -	-	-	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
592	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE , G	04/2011	166.89 -	166.89	.02	- -	-	-	0/0
593	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE , G	04/2007	98.74 -	381.39	312.12	- -	-	-	0/0
594	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE , G	04/2006	96.16 -	280.00	268.37	- -	-	-	0/0
595	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE , G	04/2012	1,054.35 -	2,200.00	85.33	- -	-	-	0/0
596	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE , G	04/2012	923.23 -	923.23	1.11	- -	-	-	0/1
597	DELHI-SOHNNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE , G	04/2013	1,239.00 -	1,239.00	-	- -	-	-	0/0
598	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE , G	04/2007	336.91 -	336.91	143.18	- -	-	-	0/0
599	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE , G	04/2013	296.00 -	466.65	-	- -	-	-	0/0
600	RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE , G	04/2007	970.34 -	1,714.49	613.36	- -	-	-	0/2
601	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE , G	04/2010	337.49 -	792.01	1.13	- -	-	-	0/1
602	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE , G	04/2008	2,050.00 -	2,050.00	200.35	- -	-	-	0/1
603	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE , G	04/2010	338.54 -	338.54	212.64	- -	-	-	0/0
604	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE , G	04/2008	162.96 -	162.96	153.31	- -	-	-	0/0
605	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE , G	04/2013	876.00 -	876.00	-	- -	-	-	0/0
606	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE , G	04/2007	328.14 -	1,540.00	45.20	- -	-	-	0/0
607	MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE , G	04/2012	250.93 -	259.23	8.43	- -	-	-	0/0
608	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE , G	04/2007	313.24 -	554.70	342.00	01/1999 -	-	-	0/0
609	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE , G	04/2008	466.48 -	750.00	-	01/1999 -	-	-	0/0
610	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE , G	05/2015	600.00 -	648.00	.94	- -	03/2020	-	0/0
611	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE , G	03/2015	1,830.00 1,190.92	1,190.92	84.05	- -	-	-	0/0
612	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE , G	05/2015	860.43 -	860.43	301.48	- -	03/2020	-	0/0
613	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE , G	03/2015	1,618.00 1,614.59	1,614.59	456.03	- -	-	-	0/0
614	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE , G	05/2015	720.00 -	678.54	-	- -	12/2018	-	0/38
615	DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE , Central Sector Projects	10/2006	81,459.00 -	28,181.00	-	- -	-	-	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
616	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE , G	04/2015	2,063.03 -	2,063.03	.14	- -	03/2021	- -	0/0
617	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE , G	04/2015	636.38 -	636.38	-	- -	-	-	0/0
618	DUDHNOI-MENDHIPATHAR - [N22000378]NFR,MULTI STATE , G	04/1992	315.64 -	315.00	308.58	- -	11/2014	-	0/0
619	HARMUTI-NAHARLAGUN - [N22000382]NFR,MULTI STATE , G	04/2006	614.54 -	613.00	553.34	- -	03/2014	-	0/0
620	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND , G	04/2006	850.00 -	3,000.00	368.41	03/2015 -	03/2020	60(O) -	0/0
621	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND , G	04/2013	4,274.00 -	4,274.00	-	- -	03/2020	- -	0/0
622	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA , G	04/1994	470.21 -	3,004.90	914.57	- -	06/2021	- -	0/0
623	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA , G	04/1996	301.64 -	1,185.64	-	- 09/2009	03/2019	- 114(R)	0/0
624	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA , G	04/1999	166.16 -	380.00	369.49	02/2009 02/2009	06/2017	-	0/1
625	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA , G	04/1998	183.23 -	1,202.70	482.09	02/2015 -	12/2019	58(O) -	0/0
626	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA , G	04/2000	133.41 207.00	340.00	-	03/2009 03/2009	12/2017	105(O) 105(R)	1/1
627	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA , G	04/2005	810.78 -	1,928.07	466.10	- -	12/2022	- -	0/0
628	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA , G	04/2010	149.90 -	230.00	54.96	03/2015 -	-	-	0/0
629	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA , G	03/2011	679.27 -	1,579.27	561.78	- -	03/2021	- -	0/0
630	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA , G	03/2013	858.67 -	843.04	41.36	- -	03/2021	- -	0/0
631	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA , G	03/2006	201.00 -	230.00	242.28	- -	-	-	0/0
632	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA , G	03/2012	155.81 -	238.03	150.50	- -	03/2020	- -	0/0
633	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA , G	03/2011	165.16 -	234.71	224.64	03/2015 -	-	-	0/0
634	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA , G	04/2015	1,547.38 -	1,547.38	34.69	03/2021 -	03/2021	0(O) -	0/0
635	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA , G	04/2015	2,361.74 -	2,361.74	17.49	03/2021 -	03/2022	12(O) -	0/0
636	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA , G	04/2015	701.61 -	701.61	37.66	03/2021 -	03/2021	0(O) -	0/0
637	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA , G	04/2015	1,172.92 -	1,172.92	74.32	03/2021 -	03/2020	-12(O) -	0/0
638	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA , G	11/2015	969.83 -	969.83	82.00	03/2020 -	03/2020	0(O) -	0/0
639	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]SER,ODISHA , G	04/1995	524.43 -	939.00	183.99	12/2021 -	12/2021	0(O) -	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
640	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA , G	01/1991	2,335.67 -	2,335.67	19.87	- -	12/2024	- -	0/0
641	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA , G	03/2006	960.18 -	960.18	609.51	03/2020 -	03/2020	0(O) -	0/0
642	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA , G	03/2009	942.95 -	942.95	.16	03/2019 -	03/2019	0(O) -	0/0
643	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]ECOR,ODISHA , G	04/2016	5,200.00 -	5,200.00	-	03/2020 -	03/2020	0(O) -	0/0
644	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB , G	04/2009	396.04 -	369.00	186.27	- -	-	-	0/0
645	QADIAN-BEAS - [N22000295]NR,PUNJAB , G	04/2011	205.22 -	205.22	1.59	- -	-	-	0/0
646	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN , G	02/1997	410.08 -	780.98	372.98	- -	08/2018	- -	0/0
647	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN , G	04/2008	829.74 -	1,161.64	456.30	03/2015 -	12/2019	57(O) -	0/0
648	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN , G	04/2008	653.19 -	941.04	653.42	03/2014 -	06/2019	63(O) -	0/0
649	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN , G	04/2008	516.23 -	735.00	694.13	03/2014 -	-	-	0/0
650	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN , G	04/2012	246.08 -	348.55	30.25	- -	03/2019	- -	0/0
651	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN , G	04/2013	236.93 -	276.89	100.50	- -	10/2018	- -	0/0
652	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN , G	04/2013	822.00 -	822.00	-	- -	-	-	0/1
653	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN , G	04/2013	323.00 -	323.00	-	- -	-	-	0/0
654	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN , G	04/2013	456.00 -	855.16	594.36	- -	05/2018	- -	0/0
655	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN , G	04/2010	739.65 -	872.22	796.25	- -	-	-	0/1
656	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN , G	04/2011	213.39 -	272.99	94.92	- -	03/2019	- -	0/0
657	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN , G	04/2012	288.97 335.53	369.08	165.53	- -	10/2018	- -	0/0
658	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN , G	04/2013	242.09 -	293.68	128.27	- -	03/2019	- -	0/0
659	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN , G	05/2015	873.71 -	873.71	-	- -	-	-	0/0
660	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN , G	01/2011	493.17 -	493.17	383.12	03/2018 -	03/2018	0(O) -	0/0
661	MULTI MODAL LOGISTICS PARK AT SWARUPGANJ - [N22000423]CCOI,RAJASTHAN , G	04/2012	471.82 -	471.82	19.91	03/2019 -	03/2019	0(O) -	0/0
662	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM , G	04/2008	1,339.48 -	4,084.69	383.92	12/2015 -	03/2020	51(O) -	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
663	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU , G	02/1997	155.55 -	920.00	855.00	- -	-	-	0/0
664	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU , G	04/2006	495.74 495.74	732.89	407.91	06/2013 -	03/2018	57(O) -	1/4
665	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU , G	09/2007	404.19 -	2,072.50	965.52	- -	-	-	0/0
666	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU , G	09/2006	343.17 -	1,065.00	1,051.14	- -	-	-	0/0
667	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU , G	09/2006	456.00 582.83	2,300.00	228.81	- 07/2008	-	-	0/0
668	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU , G	04/2008	446.87 527.37	527.37	3.34	- 01/2011	-	-	0/0
669	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU , G	04/2013	839.00 -	1,500.00	.61	- -	-	-	0/0
670	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU , G	04/1998	271.24 -	520.00	464.68	- -	-	-	0/0
671	ERODE-PALANI - [N22000199]SR,TAMIL NADU , G	04/2008	288.57 -	603.22	1.63	- -	-	-	0/0
672	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU , G	04/2008	164.41 -	302.90	35.93	- -	-	-	0/0
673	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]RVNL,TAMIL NADU , G	04/2011	190.10 -	350.00	286.57	- -	03/2019	- -	0/0
674	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA , G	12/1994	124.43 -	1,010.00	919.06	- -	-	-	0/0
675	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA , G	07/1998	125.00 -	480.00	3.48	07/2008 -	-	-	0/0
676	MANOHARABAD-KOTHPALLI NEW LINE(SCR) - [N22000032]SCR,TELANGANA , G	04/2006	378.56 -	1,160.47	1.74	- -	03/2022	- -	0/1
677	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA , G	04/2012	632.68 -	816.55	461.84	03/2016 -	12/2018	33(O) -	0/0
678	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA , G	04/2013	1,112.00 -	1,112.00	.36	- -	-	-	0/1
679	KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA , G	04/2013	616.08 -	616.08	.36	- -	-	-	0/1
680	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES,TELANGANA , G	03/2015	636.38 -	636.38	169.16	03/2021 -	03/2021	0(O) -	3/3
681	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA , G	04/2015	728.10 -	728.10	25.08	12/2024 -	12/2024	0(O) -	0/0
682	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA , G	04/2008	813.34 -	3,451.00	2,365.89	03/2014 -	03/2020	72(O) -	0/0
683	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA , G	04/1999	895.00 -	1,857.00	1,489.68	03/2007 -	04/2016	-	0/0
684	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA , G	04/2012	252.00 -	580.00	-	- -	07/2019	- -	2/3
685	KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER,UTTAR PRADESH , G	03/1997	677.97 1,062.36	1,679.13	1,706.54	- -	-	-	0/0
686	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH , G	04/1999	108.00 -	432.72	446.52	12/2009 -	-	-	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
687	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH , G	04/1997	120.00 -	245.39	210.67	12/2008 -	-	-	0/0
688	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH , G	04/2006	325.00 -	1,581.53	618.19	03/2010 -	-	-	0/0
689	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH , G	02/2008	171.10 -	275.08	141.55	03/2012 -	-	-	0/0
690	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH , G	03/2013	307.00 -	308.00	-	-	-	-	0/0
691	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH , G	03/2008	195.64 -	474.30	405.98	-	03/2018	-	0/0
692	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH , G	03/2012	199.75 -	199.75	215.55	-	03/2018	-	0/0
693	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH , G	03/2013	643.00 -	644.00	-	-	-	-	0/0
694	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH , G	04/2012	377.44 -	377.44	182.85	-	-	-	0/0
695	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH , G	04/2013	654.00 -	654.00	-	-	-	-	0/0
696	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH , G	04/2012	380.00 -	380.00	4.12	-	-	-	0/0
697	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH , G	04/2014	182.92 -	197.73	-	-	-	-	0/0
698	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]NER,UTTAR PRADESH , G	04/1997	836.26 -	1,072.52	1,026.65	-	-	-	0/0
699	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH , G	03/2015	1,750.00 -	1,295.42	19.80	03/2022 -	03/2022	0(O)	0/0
700	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR,UTTAR PRADESH , G	04/2015	524.00 668.00	668.00	-	03/2020 -	03/2020	0(O)	0/6
701	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH , G	04/2015	750.55 -	750.56	20.42	12/2024 -	12/2024	0(O)	0/0
702	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH , G	04/2011	927.01 -	977.00	739.55	03/2019 -	03/2019	0(O)	0/0
703	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH , G	04/2015	1,765.90 -	1,765.90	32.39	12/2025 -	12/2025	0(O)	0/0
704	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH , G	03/2012	1,183.25 -	1,183.30	729.14	12/2020 -	12/2020	0(O)	0/0
705	RAMNA - SINGRAULI DOUBLING - [N22000417]JECR,UTTAR PRADESH , G	08/2015	2,436.21 -	2,436.21	79.66	03/2020 -	03/2020	0(O)	0/0
706	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]JECR,UTTAR PRADESH , G	08/2015	528.57 -	528.57	61.44	03/2018 -	03/2019	12(O)	0/0
707	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND , G	04/2003	142.45 -	228.40	.15	-	-	-	0/0
708	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND , G	04/2012	219.83 -	346.63	38.33	-	-	-	0/0
709	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND , G	04/2011	4,295.30 -	1,621.60	217.35	12/2026 -	12/2026	0(O)	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
710	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL , G	04/1983	36.80 274.41	614.00	261.72	- -	-	-	0/0
711	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL , G	04/1974	393.46 154.30	1,026.00	182.48	03/2007 03/2007	-	-	0/0
712	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL , G	03/2000	1,049.69 -	3,404.92	3,544.30	12/2006 -	-	-	0/0
713	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL , G	04/2000	1,188.91 -	1,319.33	757.23	- 12/2009	03/2019	- 111(R)	0/0
714	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL , G	04/2007	1,106.62 -	1,106.62	355.85	12/2010 -	-	-	3/7
715	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL , G	03/1984	293.97 -	749.69	-	06/2005 -	-	-	0/0
716	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL,WEST BENGAL , G	04/2010	2,397.72 -	2,397.72	197.20	03/2016 -	-	-	0/0
717	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL , G	04/2010	2,298.42 -	2,733.86	40.17	03/2014 -	-	-	0/0
718	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL , G	04/2010	3,951.98 -	4,259.48	1,464.73	03/2016 -	12/2020	57(O) -	0/0
719	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL , G	04/2010	2,913.51 -	2,913.50	714.40	03/2016 -	12/2018	33(O) -	0/0
720	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER,WEST BENGAL , G	04/2009	533.38 -	533.38	127.10	12/2011 -	-	-	0/0
721	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL , G	04/2009	611.03 -	611.03	146.31	12/2011 -	-	-	0/0
722	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER,WEST BENGAL , G	04/2004	293.74 -	229.33	140.60	12/2010 -	-	-	0/0
723	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL , G	04/1999	207.52 -	334.87	293.47	12/2012 -	-	-	0/0
724	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL , G	03/2013	4,874.58 -	4,874.58	1,881.65	03/2016 -	06/2018	27(O) -	0/0
725	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL , G	04/2010	267.37 -	434.00	40.66	- -	-	-	0/0
726	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL , G	04/2011	289.64 -	760.00	.13	- -	-	-	0/0
727	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]RVNL,WEST BENGAL , G	04/2010	171.02 -	250.00	241.47	06/2013 -	12/2016	-	0/0
728	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL , G	04/2010	221.42 -	380.00	32.45	- -	-	-	0/0
729	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR,WEST BENGAL , G	04/2011	209.77 -	630.00	393.80	- -	03/2018	-	0/0
730	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR,WEST BENGAL , G	04/2012	283.55 -	450.00	194.56	- -	03/2019	-	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
731	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL , G	04/2009	573.78 -	268.52	.67	- -	-	-	0/0
732	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL , G	04/2012	255.64 -	272.20	.64	- -	-	-	0/0
733	MM FROM PANSKURA-GHATAL NL - [N22000309]SER, WEST BENGAL , G	04/2011	276.69 -	426.00	-	01/1999 -	-	-	0/0
734	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR, WEST BENGAL , G	04/2016	556.31 -	612.00	-	- -	-	-	0/0
735	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]SER, WEST BENGAL , G	01/1991	763.18 -	1,428.00	482.05	12/2021 -	12/2021	0(O) -	0/0
736	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER, WEST BENGAL , G	04/1998	1,027.40 -	2,373.00	483.01	03/2003 -	-	-	0/0
	Total		3,53,681.04 -	4,65,297.26	1,38,934.44				13/109
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
737	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, ANDHRA PRADESH , PPP (BOT)	11/2010	1,585.00 -	1,585.00	2,284.33	05/2013 -	12/2017	55(O) -	0/0
738	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI, ANDHRA PRADESH , PPP (BOT)	04/2011	571.00 -	571.00	622.89	10/2013 -	12/2017	50(O) -	0/0
739	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI, ANDHRA PRADESH , PPP (BOT)	11/2011	1,535.00 -	1,535.00	3,123.77	05/2014 -	06/2017	-	0/0
740	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH, ANDHRA PRADESH , EPC	12/2014	201.12 201.00	201.12	-	02/2015 -	-	-	0/4
741	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]PWD, ANDHRA PRADESH , G	02/2015	241.61 -	241.61	7.71	02/2017 -	02/2017	-	0/1
742	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265]PWD, ANDHRA PRADESH , EPC	11/2014	297.78 330.00	330.00	-	02/2017 -	02/2017	-	0/0
743	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD, ANDHRA PRADESH , G	01/2014	361.30 200.69	207.40	44.08	07/2014 -	-	-	0/1
744	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) - [N24000267]PWD, ANDHRA PRADESH , EPC	02/2014	258.99 -	258.99	16.54	07/2014 -	07/2016	-	0/1
745	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD, ANDHRA PRADESH , EPC	07/2014	251.55 -	251.55	7.74	02/2015 -	02/2017	-	0/1

Detail of ongoing Projects Costing Rs150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
746	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH , EPC	03/2015	175.03 -	175.00	-	-	-	-	0/1
747	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP - [N24000272]PWD,ANDHRA PRADESH , EPC	02/2015	266.00 -	266.00	-	-	-	-	0/4
748	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH , EPC	07/2015	314.43 -	314.43	-	-	-	-	0/0
749	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH , G	07/2015	333.21 333.21	333.21	-	12/2015 -	12/2016	-	0/2
750	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH , EPC	01/2014	195.45 -	195.45	-	11/2014 -	11/2016	-	0/4
751	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH , EPC	02/2014	170.21 -	170.21	5.65	11/2014 -	11/2016	-	0/4
752	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH , EPC	10/2015	480.21 -	480.21	-	-	-	-	0/0
753	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH , EPC	02/2015	224.83 -	224.83	-	05/2015 -	05/2017	-	2/4
754	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU - [N24000300]PWD,ANDHRA PRADESH , EPC	03/2015	309.01 -	309.01	-	09/2015 -	08/2017	-	0/4
755	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH , EPC	03/2015	271.45 -	271.45	-	10/2015 -	10/2017	24(O) -	0/0
756	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH.0) - [N24000302]PWD,ANDHRA PRADESH , G	07/2015	333.21 -	333.21	-	12/2015 -	12/2016	-	0/0
757	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH , EPC	02/2014	417.61 -	417.61	-	06/2014 -	06/2016	-	0/2
758	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH , EPC	10/2015	333.21 -	333.21	-	11/2015 -	11/2015	-	0/0
759	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH , EPC	02/2015	224.83 -	224.83	-	04/2015 -	05/2016	-	0/0
760	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH , G	01/2016	1,134.97 -	1,134.97	200.04	-	11/2018	-	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
761	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH , G	09/2014	1,684.00 -	1,684.00	54.13	02/2017 -	02/2017	-	0/0
762	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]NHAI,ANDHRA PRADESH , G	03/2017	648.32 -	503.10	-	03/2020 -	03/2020	0(O) -	0/0
763	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH , G	03/2017	1,041.62 -	1,187.10	-	03/2020 -	03/2020	0(O) -	0/0
764	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH , Central Sector Projects	06/2017	648.33 -	648.33	-	06/2017 -	06/2017	-	0/0
765	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2011	156.63 276.00	276.00	132.21	02/2012 -	-	-	0/0
766	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH , ITEM RATE	11/2010	305.49 -	305.49	-	03/2011 -	-	-	0/0
767	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH , ITEM RATE	03/2012	207.03 -	207.03	-	05/2012 -	-	-	0/0
768	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	194.11 -	194.11	30.54	05/2018 -	05/2018	0(O) -	1/4
769	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL,ARUNACHAL PRADESH , EPC	10/2015	179.82 -	179.82	8.99	01/2019 -	01/2019	0(O) -	1/4
770	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH , EPC	07/2015	197.16 -	197.16	38.50	10/2018 -	10/2018	0(O) -	1/4
771	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	394.00 -	394.00	-	06/2018 -	06/2018	0(O) -	0/3
772	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH , ITEM RATE	01/2011	264.16 -	264.16	-	-	-	-	0/0
773	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2009	165.00 -	165.00	-	09/2010 -	09/2010	-	0/0
774	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2009	104.00 -	201.00	-	09/2010 -	09/2010	-	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
775	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	235.08 -	235.08	47.81	05/2018 -	05/2018	0(O) -	1/4
776	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROMKM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH , G	01/2016	183.65 -	183.65	-	11/2016 -	11/2016	-	0/0
777	FUNDED) 2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE - [N24000615]NHIDCL,ARUNACHAL PRADESH , G	01/2016	334.22 -	334.22	-	06/2016 -	06/2016	-	0/4
778	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH , G	04/2016	245.79 -	245.79	-	-	-	-	0/0
779	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH , G	04/2016	198.00 -	198.00	-	10/2016 -	10/2016	-	0/4
780	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH , G	11/2015	434.06 -	434.06	-	-	-	-	0/0
781	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH , G	12/2016	138.93 155.00	155.00	-	01/2017 -	01/2020	36(O) -	0/0
782	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH , G	01/2017	1,253.10 -	1,253.10	-	03/2017 -	-	-	0/0
783	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH , G	03/2017	284.09 -	284.09	-	04/2017 -	-	-	0/0
784	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH , G	02/2017	195.23 -	195.23	-	04/2017 -	-	-	0/0
785	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH , G	02/2017	203.36 -	203.36	-	04/2017 -	-	-	0/0
786	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH , G	01/2017	194.66 -	194.66	-	04/2017 -	-	-	0/0
787	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH , G	02/2017	168.32 -	168.32	-	04/2017 -	-	-	0/0
788	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH , G	02/2017	180.57 -	180.57	-	04/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
789	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH , G	02/2017	216.71 -	216.71	-	04/2017 -	-	-	0/0
790	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH , G	02/2017	167.28 -	167.28	-	04/2017 -	-	-	0/0
791	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH , G	01/2017	198.22 -	198.22	-	04/2017 -	-	-	0/0
792	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM , G	12/2003	280.00 -	361.00	410.80	02/2009 -	12/2017	106(O) -	0/0
793	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM , G	12/2003	199.81 -	385.13	214.03	04/2009 -	12/2017	104(O) -	0/0
794	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM , G	12/2003	167.64 -	167.64	276.13	11/2008 -	11/2017	108(O) -	0/0
795	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM , G	12/2003	155.04 -	280.13	195.35	11/2008 -	03/2018	112(O) -	0/0
796	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM , G	12/2003	200.00 -	200.00	250.85	04/2009 -	12/2017	104(O) -	0/0
797	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM , G	12/2003	245.00 -	245.00	216.62	03/2008 -	11/2017	116(O) -	0/0
798	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM , G	12/2003	225.00 -	225.00	314.51	06/2008 -	10/2017	112(O) -	0/0
799	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM , G	12/2003	208.00 -	208.00	-	04/2008 -	12/2017	116(O) -	0/0
800	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM , G	12/2003	160.00 -	160.00	205.46	05/2008 -	02/2018	117(O) -	0/0
801	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM , G	12/2003	196.00 -	331.23	342.62	07/2009 -	12/2017	101(O) -	0/0
802	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM , G	12/2003	217.61 -	309.56	389.87	04/2010 -	03/2018	95(O) -	0/0
803	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM , EPC	05/2015	454.89 -	454.89	22.74	05/2018 -	05/2018	0(O) -	0/4
804	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM , EPC	06/2015	437.39 -	437.39	21.86	06/2018 -	06/2018	0(O) -	0/4
805	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM , EPC	06/2015	463.49 -	463.49	9.26	06/2018 -	06/2018	0(O) -	0/4
806	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL,ASSAM , EPC	06/2016	829.00 -	829.00	59.85	01/2019 -	01/2019	0(O) -	0/4
807	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM , EPC	03/2015	168.39 -	168.39	16.84	11/2018 -	11/2018	0(O) -	0/4
808	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM , EPC	10/2014	588.95 -	588.95	80.00	11/2018 -	11/2018	0(O) -	0/4

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
809	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM , EPC	11/2010	268.08 -	268.08	-	05/2017 -	05/2017	-	0/0
810	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAF LONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM , ITEM RATE	11/2010	470.20 -	470.20	-	02/2011 -	02/2011	-	0/0
811	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM , ITEM RATE	05/2011	176.22 -	176.22	-	02/2018 -	02/2018	0(O) -	0/0
812	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM , EPC	11/2014	218.31 -	218.31	-	02/2018 -	02/2018	0(O) -	0/0
813	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]NHIDCL,ASSAM , EPC	12/2015	225.02 -	159.20	-	12/2018 -	12/2018	0(O) -	0/4
814	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM , EPC	12/2015	223.30 -	223.30	-	06/2018 -	06/2018	0(O) -	0/0
815	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM , EPC	01/1991	520.01 -	520.01	-	-	-	-	0/0
816	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM , EPC	12/2015	289.99 -	289.99	-	12/2018 -	12/2018	0(O) -	0/0
817	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM , EPC	01/2016	294.17 -	294.17	-	01/2016 -	01/2016	-	0/4
818	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM , EPC	01/2016	252.00 -	252.00	-	01/2016 -	01/2016	-	0/4
819	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR , PPP (ANNUITY)	08/2010	671.30 -	671.30	-	02/2013 -	06/2018	64(O) -	0/0
820	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR , PPP (ANNUITY)	05/2011	351.54 -	351.54	-	05/2013 -	10/2017	53(O) -	0/0
821	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR , PPP (ANNUITY)	05/2011	664.00 -	664.00	-	02/2014 -	-	-	0/0
822	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR , PPP (BOT)	09/2011	574.00 -	574.00	-	03/2014 -	09/2017	-	0/0
823	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR , G	10/2011	375.09 -	375.09	-	04/2014 -	-	-	0/0
824	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR , PPP (ANNUITY)	01/2011	575.00 -	575.00	-	07/2013 -	03/2018	56(O) -	0/0
825	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR , PPP (ANNUITY)	05/2011	511.54 -	511.54	-	11/2013 -	12/2017	49(O) -	0/0
826	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR , EPC	01/1991	675.00 -	675.00	-	-	-	-	0/0
827	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR , ITEM RATE	01/1991	282.41 -	282.41	67.52	08/2016 -	08/2016	-	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
828	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR , ITEM RATE	01/1991	358.22 -	358.22	188.71	10/2016 -	10/2016	-	0/0
829	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR , G	08/2015	556.07 -	556.07	-	- -	-	-	0/0
830	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR , G	12/2015	1,041.10 -	1,041.10	-	- -	04/2019	-	0/0
831	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR , G	08/2015	814.04 -	814.04	-	- -	-	-	0/0
832	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR , G	08/2015	322.09 -	322.09	-	- -	04/2018	-	0/0
833	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR , G	01/1991	642.41 -	642.41	-	- -	-	-	0/0
834	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR , G	12/2015	1,167.45 -	1,167.45	-	- -	-	-	0/0
835	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR , G	08/2015	399.54 -	399.54	-	- -	04/2019	-	0/0
836	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR , G	01/1991	478.35 -	478.35	-	- -	-	-	0/0
837	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR , G	08/2015	854.80 -	854.80	-	- -	12/2017	-	0/0
838	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR , G	08/2015	516.13 -	516.13	-	- -	04/2018	-	0/0
839	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR , EPC	01/1991	154.62 -	154.62	-	- -	-	-	0/0
840	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR , EPC	01/1991	319.68 -	319.68	-	- -	-	-	0/0
841	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR , G	10/2014	377.64 -	377.64	-	03/2014 -	-	-	0/0
842	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR , G	10/2013	278.39 -	278.39	-	08/2014 -	08/2014	-	0/0
843	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR , G	01/2013	322.01 -	322.01	-	08/2014 -	-	-	0/0
844	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR , G	11/2013	683.83 -	683.83	-	07/2016 -	-	-	0/0
845	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR , G	02/2014	665.50 -	665.50	-	07/2016 -	-	-	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
846	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR , G	02/2016	178.85 -	178.85	-	05/2016 -	-	-	0/0
847	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR , G	02/2016	369.77 -	369.77	-	06/2016 -	06/2016	-	0/0
848	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR , G	02/2016	553.30 -	553.30	-	05/2016 -	-	-	0/0
849	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR , G	01/2014	1,408.85 -	1,408.85	-	10/2016 -	-	-	0/0
850	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPROV - [N24000580]MORTH,BIHAR , G	03/2015	206.80 -	206.80	-	07/2016 -	10/2016	-	0/0
851	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR , G	08/2015	288.24 -	288.24	-	11/2015 -	-	-	0/0
852	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI,BIHAR , G	05/2015	581.84 -	581.84	-	05/2017 -	-	-	0/0
853	REHABILATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR , G	08/2016	1,742.01 -	1,742.01	-	12/2016 -	12/2016	-	0/0
854	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR , G	03/2017	672.89 -	736.01	-	03/2020 -	03/2020	0(O) -	0/0
855	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR , G	03/2017	235.48 -	227.77	-	03/2020 -	03/2020	0(O) -	0/0
856	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR , Central Sector Projects	08/2017	950.64 -	950.64	-	08/2017 -	08/2017	-	0/0
857	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH , EPC	10/2014	213.47 -	213.47	-	03/2015 -	03/2015	-	0/0
858	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH , EPC	10/2014	298.34 -	298.34	-	03/2015 -	03/2015	-	0/0
859	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH , EPC	11/2014	262.54 -	262.54	-	03/2015 -	03/2015	-	0/0
860	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH , EPC	12/2015	291.05 -	291.05	-	- -	-	-	0/0
861	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- [N24000283]PWD,CHHATISGARH , ITEM RATE	12/2010	169.26 -	169.26	-	12/2012 -	-	-	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
862	REHABILITATION AND UP GRADATION OF NH-12A FROM KM.246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH , EPC	12/2014	394.20 -	394.20	-	- -	-	-	0/0
863	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH , EPC	11/2015	485.44 -	485.44	-	12/2015 -	-	-	0/0
864	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH , EPC	03/2015	422.34 -	422.34	22.25	- -	-	-	0/0
865	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATISGARH , G	02/2013	1,232.00 -	1,232.00	-	08/2015 -	12/2017	28(O) -	0/0
866	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH , G	12/2015	596.67 -	596.67	-	- -	05/2018	- -	0/0
867	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH , G	12/2015	509.13 -	509.13	-	- -	04/2018	- -	0/0
868	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH , G	12/2015	726.67 -	726.67	-	- -	04/2018	- -	0/0
869	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I) , NEW - [N24000609]NHAI,DELHI , G	09/2015	771.18 -	771.18	559.96	- -	03/2018	- -	0/0
870	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDEAPAR BRIDGE - [N24000251]NHDP,GOA , EPC	03/2015	297.00 -	297.00	38.33	- -	04/2018	- -	0/1
871	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA , G	03/2015	298.33 -	298.33	16.10	- -	-	-	0/4
872	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]DORTH,GOA , EPC	03/2015	184.05 -	184.05	10.72	- -	-	-	0/4
873	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA , EPC	03/2015	280.16 -	280.16	16.06	- -	-	-	0/4
874	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA , EPC	10/2015	936.40 -	936.40	-	- -	-	-	0/0
875	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA , EPC	12/2015	773.98 -	773.98	-	- -	-	-	0/0
876	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA , EPC	12/2015	819.95 -	819.95	-	- -	-	-	0/0
877	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT , PPP (BOT)	03/2010	1,509.10 -	3,237.87	-	09/2012 -	12/2017	63(O) -	2/3
878	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT , PPP (BOT)	01/2011	953.88 -	953.88	-	07/2013 -	-	-	0/0
879	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT , PPP (BOT)	01/2013	2,125.24 -	2,125.24	-	12/2015 -	07/2017	-	0/3
880	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT , G	03/2014	503.16 -	503.16	-	08/2016 -	-	-	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
881	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT , G	05/2016	998.18 -	998.18	-	-	-	-	0/0
882	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT , G	05/2016	834.64 -	834.64	-	-	-	-	0/0
883	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT , G	05/2016	723.64 -	723.64	-	-	-	-	0/0
884	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT , G	05/2016	763.08 -	763.08	-	-	-	-	0/0
885	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT , G	05/2016	425.60 -	425.60	-	-	-	-	0/0
886	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT , G	05/2016	364.56 -	364.56	-	-	-	-	0/0
887	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT , G	07/2016	829.97 -	829.97	-	-	-	-	0/0
888	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT , G	12/2016	417.19 -	417.19	-	-	-	-	0/0
889	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT , G	01/2017	1,251.11 -	1,251.11	-	-	-	-	0/0
890	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT , G	06/2017	1,958.88 -	1,958.88	-	06/2020 -	06/2020	0(O) -	0/0
891	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT , Central Sector Projects	10/2017	232.49 -	232.49	-	10/2017 -	10/2017	0(O) -	0/0
892	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA , PPP (BOT)	04/2007	486.00 -	486.00	481.87	05/2010 -	08/2017	-	0/0
893	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA , PPP (BOT)	05/2009	1,108.00 -	2,288.00	3,882.53	11/2011 -	03/2018	76(O) -	0/0
894	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA , PPP (BOT)	05/2011	650.00 -	650.00	832.39	11/2013 -	08/2017	-	0/0
895	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA , G	08/2015	723.54 -	723.54	562.23	02/2018 -	02/2018	0(O) -	0/0
896	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA-BARWALA - PANCHKULA(PKG - 2) - [N24000358]NHAI,HARYANA , G	10/2015	562.34 -	562.34	292.94	04/2018 -	04/2018	0(O) -	0/0
897	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA , G	12/2015	602.95 -	602.95	266.77	06/2016 -	06/2018	24(O) -	0/0
898	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA , G	01/2016	574.28 -	574.28	204.29	07/2018 -	07/2018	0(O) -	0/0
899	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA , PPP (BOT)	07/2015	2,128.72 -	2,128.72	249.15	-	04/2019	-	0/0
900	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI,HARYANA , PPP (BOT)	07/2015	1,393.00 -	1,393.00	2,262.08	-	01/2018	-	0/0
901	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA , G	11/2015	867.66 -	867.66	562.35	-	05/2018	-	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
902	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA-BARWALA - PANCHKULA (PKG - 1) - [N24000597]NHAI,HARYANA , G	05/2015	600.85 -	600.85	264.53	- -	05/2018	- -	0/0
903	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA , G	08/2016	248.97 -	248.97	-	- -	05/2019	- -	0/0
904	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA , G	09/2016	1,004.67 -	1,004.67	-	- -	05/2019	- -	0/0
905	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA , G	03/2017	639.79 -	552.90	12.08	03/2020 -	03/2020	0(O) -	0/0
906	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH , PPP (BOT)	11/2013	1,916.79 -	1,916.79	1,884.41	11/2016 -	02/2018	15(O) -	0/0
907	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH , G	09/2015	934.46 -	934.46	177.09	03/2018 -	03/2018	0(O) -	0/0
908	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH , G	02/2016	273.20 -	273.20	21.43	- -	02/2019	- -	0/0
909	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH , G	08/2016	1,583.18 -	1,583.18	-	- -	-	- -	0/0
910	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH , G	09/2016	1,273.71 -	1,273.71	-	- -	-	- -	0/0
911	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH , G	10/2016	447.75 -	447.75	-	- -	-	- -	0/0
912	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH , G	06/2017	2,485.93 -	2,485.93	-	06/2020 -	06/2020	0(O) -	0/0
913	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,987.00 -	1,987.00	-	07/2015 -	03/2019	44(O) -	0/0
914	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	05/2011	2,159.00 -	2,159.00	-	06/2015 -	-	- -	0/0
915	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,813.76 -	1,813.76	-	07/2013 -	11/2017	52(O) -	0/0
916	SRINAGAR TO BANIHAI - [N24000189]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	06/2011	1,100.70 -	1,100.70	-	06/2014 -	12/2017	42(O) -	0/0
917	FOUR LANING OF RAMBAN - BANIHAI SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR , G	12/2015	2,168.66 -	2,168.66	-	06/2019 -	06/2019	0(O) -	0/0
918	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR , G	12/2015	2,136.97 -	2,136.97	-	12/2018 -	12/2018	0(O) -	0/0
919	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND , PPP (ANNUITY)	12/2012	1,479.00 -	1,479.00	842.15	06/2015 -	12/2017	30(O) -	0/0
920	TWO LANE WITH PAVED SHOULDERS OF CHAS - RAMGARH SECTION OF NH-23 - [N24000343]NHAI,JHARKHAND , G	09/2015	341.61 -	341.61	308.23	09/2017 -	09/2017	- -	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
921	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND , G	02/2016	997.15 -	997.15	270.45	- -	03/2019	- -	0/0
922	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND , G	07/2016	458.03 -	458.03	-	- -	-	-	0/0
923	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND , G	08/2016	323.72 -	323.72	9.23	- -	08/2018	- -	0/0
924	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]NHAI,JHARKHAND , G	03/2017	165.50 -	172.16	-	03/2020 -	03/2020	0(O) -	0/0
925	4 LANING OF KUTCERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI,JHARKHAND , G	03/2017	239.68 -	235.90	-	03/2020 -	03/2020	0(O) -	0/0
926	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA , G	09/2010	946.00 -	946.00	-	- -	12/2017	- -	3/3
927	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA , EPC	03/2015	165.67 -	165.67	-	11/2015 -	11/2017	24(O) -	0/0
928	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA , EPC	03/2015	159.12 -	159.12	-	11/2015 -	11/2017	24(O) -	0/0
929	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA , G	05/2015	709.00 -	709.00	-	09/2017 -	09/2017	-	0/0
930	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA , EPC	01/1991	219.40 -	219.40	-	01/2018 -	01/2018	0(O) -	0/0
931	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA , PPP (BOT)	05/2014	1,655.01 -	1,655.01	-	08/2016 -	03/2018	19(O) -	0/0
932	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA , PPP (BOT)	03/2015	1,388.00 -	1,388.00	-	- -	08/2018	- -	0/0
933	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA , G	03/2016	701.40 -	701.40	-	- -	-	-	0/0
934	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA , G	03/2016	870.00 -	870.00	-	- -	-	-	0/0
935	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA , G	05/2014	720.69 -	720.69	-	- -	-	-	0/0
936	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA , G	08/2016	1,664.20 -	1,664.20	-	- -	04/2019	- -	0/0
937	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA , G	08/2016	1,167.42 -	1,167.42	-	- -	03/2019	- -	0/0
938	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA , G	09/2016	950.69 -	950.69	-	- -	-	-	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
939	SIX LANING AND STRENGTHENING OF KM 340+000 TO KM 403+400 OF HUBLI-HAVERI SECTION OF NH-48 (OLD NH-4) - [N24000673]NHAI,KARNATAKA , G	03/2017	985.41 -	1,200.00	-	03/2020 -	03/2020	0(O) -	0/0
940	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA , G	03/2017	831.58 -	1,177.00	-	03/2020 -	03/2020	0(O) -	0/0
941	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA , G	03/2017	993.16 -	1,434.00	-	03/2020 -	03/2020	0(O) -	0/0
942	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA , PPP (BOT)	02/2010	617.00 -	617.00	-	08/2012 -	12/2017	64(O) -	0/0
943	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA , EPC	01/2014	255.75 348.00	348.43	.02	09/2017 -	09/2017	-	0/0
944	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA , EPC	01/2014	267.16 352.00	352.05	.02	11/2017 -	11/2017	0(O) -	0/0
945	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA , G	06/2015	845.24 -	845.24	-	- -	11/2017	- -	0/0
946	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA , G	04/2016	804.97 -	804.97	-	- -	06/2018	- -	0/0
947	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA , Central Sector Projects	09/2017	1,124.11 -	1,124.11	-	09/2017 -	09/2017	-	0/0
948	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH , PPP (BOT)	10/2010	1,175.00 -	1,206.10	-	04/2013 -	09/2017	-	0/0
949	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH , PPP (BOT)	11/2010	325.00 -	325.00	-	05/2013 -	07/2017	-	0/0
950	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH , EPC	02/2015	377.83 -	377.83	57.42	07/2017 -	07/2017	-	0/0
951	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH , BOT (TOLL)	01/2012	320.48 -	320.48	189.49	08/2015 -	09/2016	-	0/0
952	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH , EPC	06/2015	390.51 -	390.51	43.25	- -	-	-	0/0
953	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH , BOT (TOLL)	11/2011	704.26 -	704.26	-	05/2015 -	05/2015	-	0/0
954	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH , BOT (TOLL)	03/2013	257.80 -	257.80	59.30	02/2016 -	02/2016	-	0/0
955	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH , EPC	11/2013	497.05 -	497.05	-	05/2017 -	05/2017	-	0/0
956	SHAHOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH , EPC	06/2015	532.49 -	532.49	137.08	05/2017 -	05/2017	-	0/0
957	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH , BOT (TOLL)	08/2015	257.80 -	257.00	12.38	- -	-	-	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
958	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH , BOT (TOLL)	11/2011	871.15 -	871.15	332.25	09/2015 -	08/2016	-	0/0
959	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH , EPC	06/2015	641.02 -	641.02	89.88	12/2017 -	12/2017	0(O) -	0/0
960	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH , BOT (TOLL)	01/2012	381.86 -	381.86	252.03	04/2015 -	04/2015	-	0/0
961	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH , BOT (TOLL)	11/2011	670.82 -	670.82	590.00	02/2015 -	02/2015	-	0/0
962	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH , G	03/2015	795.76 -	795.76	-	-	-	-	0/0
963	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH , G	03/2015	794.30 -	794.30	-	-	-	-	0/0
964	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH , G	02/2015	327.32 -	327.32	142.73	05/2017 -	05/2017	-	0/0
965	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH , EPC	11/2015	628.45 -	628.45	20.74	03/2018 -	03/2018	0(O) -	0/0
966	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH , EPC	12/2015	927.54 -	927.54	29.17	06/2018 -	06/2018	0(O) -	0/0
967	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH , G	03/2015	928.83 -	928.83	-	-	12/2017	-	0/0
968	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH , PPP (BOT)	05/2013	1,055.00 -	1,601.77	-	11/2015 -	09/2017	-	0/0
969	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH , G	06/2015	1,012.90 -	1,012.90	-	03/2016 -	03/2019	36(O) -	0/0
970	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]NHAI,MADHYA PRADESH , PPP (BOT)	01/2016	830.36 -	830.36	-	07/2018 -	07/2018	0(O) -	0/0
971	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH , G	03/2015	810.22 -	810.22	-	-	-	-	0/0
972	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH , PPP (BOT)	06/2015	1,583.79 -	1,583.79	-	-	01/2019	-	0/0
973	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH , EPC	03/2015	511.83 -	511.83	40.87	08/2017 -	08/2017	-	0/0
974	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH , G	08/2016	227.49 -	227.49	-	-	01/2019	-	0/0
975	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH , Central Sector Projects	10/2017	639.97 -	639.97	-	10/2017 -	10/2017	0(O) -	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
976	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	374.40 -	374.40	-	09/2017 -	09/2017	-	0/0
977	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	990.61 -	990.61	-	09/2017 -	09/2017	-	0/0
978	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA , PPP (BOT)	11/2009	567.00 -	567.00	1,055.94	11/2013 -	-	-	0/0
979	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA , PPP (BOT)	10/2010	1,724.55 -	1,724.55	2,051.04	03/2013 -	12/2017	57(O) -	0/0
980	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA , G	12/2011	942.69 -	942.69	373.84	06/2014 -	03/2018	45(O) -	0/0
981	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA , PPP (BOT)	05/2013	1,348.20 -	1,348.20	1,790.50	02/2014 -	03/2018	49(O) -	2/2
982	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]NHDP,MAHARASHTRA , G	06/2014	260.39 -	260.39	87.43	11/2016 -	11/2016	-	0/2
983	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA , EPC	03/2015	168.30 -	168.30	13.43	- -	10/2017	- -	0/4
984	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOIA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA , EPC	08/2014	187.79 -	187.79	57.60	07/2016 -	07/2016	-	0/12
985	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA , EPC	01/2014	446.77 -	446.77	87.62	- -	06/2017	-	0/4
986	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]NHDP,MAHARASHTRA , EPC	12/2013	220.72 -	220.72	95.02	11/2016 -	11/2016	-	0/4
987	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA , EPC	10/2015	289.60 -	289.60	-	- -	-	-	0/0
988	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA , ITEM RATE	12/2011	156.26 227.31	156.26	65.16	- 03/2013	-	-	0/0
989	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA , ITEM RATE	03/2011	185.82 292.22	185.82	205.97	- 11/2014	11/2014	-	0/0
990	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA , EPC	01/2015	225.81 -	225.81	6.50	- -	-	-	0/0
991	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	2,288.18 -	2,288.18	-	- -	05/2019	- -	0/0
992	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA , G	09/2015	414.51 -	414.00	88.66	- -	05/2018	- -	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
993	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA , G	10/2015	531.13 -	531.13	28.10	- -	05/2018	- -	0/0
994	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA , EPC	07/2015	1,885.74 -	1,885.74	-	- -	05/2019	- -	0/0
995	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA , G	10/2015	593.26 -	593.26	-	- -	05/2018	- -	0/0
996	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA , G	12/2015	649.50 -	649.50	11.42	- -	03/2019	- -	0/0
997	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA , G	08/2015	505.00 -	505.00	76.16	- -	05/2018	- -	0/0
998	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA , PPP (BOT)	01/2015	972.50 -	972.50	1,460.25	07/2017 -	01/2018	6(O) -	0/0
999	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA , PPP (BOT)	06/2014	923.04 -	923.04	481.02	11/2016 -	11/2017	12(O) -	0/0
1000	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA , G	09/2005	168.00 -	168.00	279.92	06/2006 -	-	-	0/0
1001	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	1,871.34 -	1,871.34	2,709.38	01/2018 -	01/2018	0(O) -	0/0
1002	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA , G	04/2010	1,170.52 -	1,170.52	2,082.05	06/2012 -	03/2018	69(O) -	0/0
1003	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA , G	01/2014	292.98 -	292.98	95.60	11/2014 -	11/2014	-	0/0
1004	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA , G	03/2016	197.69 -	197.69	-	- -	07/2018	- -	0/0
1005	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA , G	03/2016	546.00 -	546.00	-	- -	07/2019	- -	0/0
1006	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA , G	03/2016	591.66 -	591.66	-	- -	07/2019	- -	0/0
1007	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR- HYDERABAD SECTION NS-60 - [N24000561]NHAI,MAHARASHTRA , G	03/2016	244.00 -	244.00	-	- -	07/2018	- -	0/0
1008	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA , G	03/2016	1,142.62 -	1,142.62	-	- -	-	-	0/0
1009	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA , G	03/2016	1,101.58 -	1,101.58	-	- -	-	-	0/0
1010	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA , G	11/2016	1,071.61 -	1,071.61	-	- -	-	-	0/0
1011	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA , G	11/2016	1,064.88 -	1,064.88	-	- -	-	-	0/0
1012	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA , G	11/2016	400.25 -	400.25	-	- -	03/2019	- -	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1013	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA , G	11/2016	446.17 -	446.17	-	- -	03/2019	- -	0/0
1014	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA , G	11/2016	290.73 -	290.73	-	- -	-	-	0/0
1015	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA , G	01/2017	244.90 -	244.90	10.85	- -	05/2019	- -	0/0
1016	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA , G	02/2017	904.16 -	904.16	-	02/2020 -	02/2020	0(O) -	0/0
1017	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA , G	03/2017	247.02 -	157.49	-	03/2020 -	03/2020	0(O) -	0/0
1018	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA , G	03/2017	744.64 -	982.00	-	03/2020 -	03/2020	0(O) -	0/0
1019	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA , G	03/2017	1,030.44 -	1,065.51	-	03/2020 -	03/2020	0(O) -	0/0
1020	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA , G	03/2017	988.34 -	1,043.28	-	03/2020 -	03/2020	0(O) -	0/0
1021	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA , G	03/2017	1,059.73 -	1,071.00	-	03/2017 -	-	-	0/0
1022	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA , G	03/2017	296.19 -	254.00	-	03/2020 -	05/2019	-10(O) -	0/0
1023	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA , G	03/2017	1,098.06 -	1,160.64	-	03/2020 -	03/2020	0(O) -	0/0
1024	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA , PPP (ANNUITY)	01/2011	536.00 -	536.00	-	01/2014 -	03/2018	50(O) -	0/0
1025	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA , ITEM RATE	12/2010	1,494.48 -	1,494.48	-	02/2011 -	02/2011	-	0/0
1026	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA , G	12/2015	479.20 -	479.20	-	- -	05/2018	- -	0/0
1027	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM , ITEM RATE	11/2010	624.41 -	624.41	-	03/2011 -	-	-	0/0
1028	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM , ITEM RATE	08/2010	193.69 -	193.69	-	10/2010 -	-	-	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1029	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM , ITEM RATE	08/2010	195.04 -	195.04	130.82	10/2010 -	10/2010	-	0/0
1030	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE , PPP (ANNUITY)	12/2003	604.00 -	604.00	-	12/2009 -	-	-	0/0
1031	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE , PPP (BOT)	02/2009	1,693.75 -	1,693.75	-	08/2011 -	09/2017	-	2/2
1032	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE , PPP (ANNUITY)	02/2011	2,498.76 -	2,498.76	-	08/2014 -	12/2017	40(O) -	0/0
1033	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE , PPP (BOT)	09/2011	2,848.00 -	2,848.00	-	03/2014 -	04/2018	49(O) -	0/0
1034	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE , PPP (BOT)	09/2011	754.00 -	754.00	1,112.95	03/2013 -	11/2017	56(O) -	0/0
1035	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE , PPP (BOT)	10/2012	1,928.22 -	1,928.22	2,488.00	04/2015 -	12/2017	32(O) -	0/0
1036	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE , EPC	03/2015	789.83 -	789.83	109.77	-	-	-	0/0
1037	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,MULTI STATE , G	09/2015	788.51 -	788.51	341.55	03/2018 -	03/2018	0(O) -	0/0
1038	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE , G	09/2016	1,244.10 -	1,244.10	-	-	-	-	0/0
1039	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND , ITEM RATE	12/2010	1,296.00 -	1,296.00	-	02/2011 -	-	-	0/0
1040	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND , G	03/2016	373.07 -	373.07	-	08/2016 -	08/2019	36(O) -	0/0
1041	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND , G	03/2016	396.52 -	396.52	-	08/2016 -	08/2019	36(O) -	0/0
1042	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND , G	03/2016	429.52 -	429.52	-	08/2016 -	08/2019	36(O) -	0/0
1043	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND , G	02/2017	507.68 -	507.68	-	04/2017 -	-	-	0/0
1044	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA , PPP (BOT)	03/2012	1,410.00 -	1,410.00	1,555.96	09/2014 -	03/2018	42(O) -	0/0
1045	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA , PPP (BOT)	12/2011	1,047.00 -	1,047.00	1,629.83	06/2014 -	12/2017	42(O) -	0/0
1046	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA , EPC	01/1991	218.63 251.92	218.63	29.27	10/2017 -	10/2017	0(O) -	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1047	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA , EPC	12/2013	319.80 -	319.80	-	10/2016 -	10/2016	-	0/0
1048	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA , G	01/1991	229.41 265.35	229.41	6.65	05/2018 -	05/2018	0(O) -	0/0
1049	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA , EPC	07/2014	342.05 -	342.05	-	01/2017 -	01/2017	-	0/0
1050	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA , G	07/2015	1,282.94 -	1,282.94	-	- -	-	-	0/0
1051	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA , G	12/2015	752.28 -	752.28	-	- -	-	-	0/0
1052	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA , EPC	12/2011	159.39 -	159.39	-	11/2017 -	11/2017	0(O) -	0/0
1053	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA , EPC	12/2011	191.08 -	191.08	-	08/2015 -	03/2018	31(O) -	0/0
1054	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA , G	02/2016	1,069.65 -	1,069.65	-	- -	-	-	0/0
1055	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA , G	09/2016	2,510.04 -	2,510.04	-	- -	08/2019	- -	0/0
1056	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA , G	10/2016	1,008.96 -	1,008.96	-	- -	-	-	0/0
1057	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA , G	03/2014	191.50 192.00	192.00	-	05/2016 -	06/2017	-	0/0
1058	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MORTH,ODISHA , G	01/2015	326.63 327.00	327.00	-	04/2018 -	04/2018	0(O) -	0/0
1059	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA , G	02/2015	239.91 240.00	240.00	-	10/2017 -	10/2017	0(O) -	0/0
1060	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH,ODISHA , G	03/2015	226.31 226.00	226.00	-	10/2017 -	10/2017	0(O) -	0/0
1061	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA , G	12/2013	319.80 320.00	320.00	-	05/2016 -	03/2017	-	0/0
1062	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA , G	07/2014	342.05 342.00	342.00	-	01/2017 -	08/2017	-	0/0
1063	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA , G	08/2013	171.96 172.00	172.00	-	06/2016 -	03/2017	-	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1064	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA , G	06/2016	157.30 157.00	157.00	-	06/2018 -	11/2018	5(O) -	0/0
1065	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH,ODISHA , G	03/2014	162.51 163.00	163.00	-	05/2016 -	03/2017	-	0/0
1066	REHABILITATION AND UPGRADE BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA , G	03/2017	1,288.07 -	1,420.00	-	03/2020 -	03/2020	0(O) -	0/0
1067	REHABILITATION AND UPGRADE OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA , Central Sector Projects	07/2017	476.56 -	476.56	-	07/2017 -	07/2017	-	0/0
1068	REHABILITATION AND UPGRADE OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB , EPC	03/2015	435.90 -	435.90	31.02	- -	-	-	0/0
1069	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB , EPC	01/2015	279.68 -	279.68	25.28	- -	-	-	0/0
1070	4-LANING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB , EPC	11/2014	463.65 546.00	463.65	280.16	- -	-	-	0/0
1071	4 LANING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB , EPC	11/2014	573.96 605.00	605.00	209.74	- -	-	-	0/0
1072	JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB , G	01/2014	523.85 -	523.85	250.08	01/2016 -	12/2017	23(O) -	0/0
1073	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB , EPC	02/2015	483.38 -	483.38	65.76	- -	-	-	0/0
1074	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB , EPC	02/2015	616.36 -	616.36	68.58	- -	-	-	0/0
1075	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB , EPC	02/2015	486.74 -	486.74	189.39	- -	-	-	0/0
1076	CONST.OF 4 LANES WITH PAVED SHOULDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB , EPC	03/2015	312.79 -	312.79	17.57	- -	-	-	0/0
1077	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOUA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB , EPC	07/2014	319.80 -	319.80	102.55	- -	-	-	0/0
1078	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB , EPC	12/2015	766.36 -	766.36	99.86	- -	-	-	0/0
1079	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB , EPC	11/2015	847.02 -	847.02	299.81	- -	-	-	0/0
1080	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB , EPC	11/2015	889.24 -	889.24	389.64	- -	-	-	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1081	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB , EPC	12/2015	578.38 -	578.38	128.53	- -	-	-	0/0
1082	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB , G	09/2015	273.06 -	273.06	55.35	- -	11/2017	- -	0/0
1083	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB , G	09/2014	479.00 -	479.00	407.76	- -	12/2017	- -	0/0
1084	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]NHAI,PUNJAB , G	12/2015	239.23 -	239.23	168.16	12/2017 -	12/2017	0(O) -	0/0
1085	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB , G	10/2015	447.29 -	447.29	51.75	12/2017 -	04/2019	16(O) -	0/0
1086	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB , EPC	06/2015	892.17 -	892.17	26.92	- -	-	-	0/0
1087	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB , EPC	06/2015	899.21 -	899.21	25.08	- -	-	-	0/0
1088	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB , G	08/2016	1,388.34 -	1,388.34	-	- -	09/2019	- -	0/0
1089	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB , G	08/2016	1,169.61 -	1,169.61	-	- -	-	-	0/0
1090	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB , G	03/2017	754.54 -	756.27	-	03/2020 -	03/2020	0(O) -	0/0
1091	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN , G	12/2003	275.00 -	281.31	-	02/2010 -	-	-	0/0
1092	DEOLI KOTA - [N24000148]NHAI,RAJASTHAN , PPP (BOT)	01/2011	593.00 -	593.00	-	07/2013 -	10/2017	51(O) -	0/0
1093	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI,RAJASTHAN , G	03/2014	240.10 -	240.10	-	03/2016 -	-	-	0/0
1094	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN , EPC	10/2014	269.22 -	269.22	33.24	01/2015 -	-	-	0/0
1095	WIDENING AND STRENGHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN , EPC	10/2014	257.09 -	257.09	14.80	01/2015 -	-	-	0/0
1096	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN , EPC	10/2013	278.87 -	278.87	-	05/2014 -	-	-	0/0
1097	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN , ITEM RATE	01/1991	376.52 -	376.52	-	04/2014 -	-	-	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1098	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN , EPC	02/2015	383.40 -	383.40	224.68	03/2015 -	-	-	0/0
1099	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN , EPC	12/2015	621.43 -	621.43	-	06/2018 -	06/2018	0(O) -	0/0
1100	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]NHAI,RAJASTHAN , G	08/2015	538.08 -	538.08	-	02/2018 -	02/2018	0(O) -	0/0
1101	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN , G	09/2014	425.19 -	425.19	-	09/2016 -	09/2017	-	0/0
1102	JAISALMER - BARMER - [N24000348]NHAI,RAJASTHAN , G	08/2015	482.27 -	482.27	-	02/2018 -	02/2018	0(O) -	0/0
1103	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]NHAI,RAJASTHAN , G	07/2015	455.60 -	455.60	-	07/2017 -	07/2017	-	0/0
1104	PADI - DAHOD - [N24000353]NHAI,RAJASTHAN , G	11/2014	279.14 -	279.14	-	05/2017 -	-	-	0/0
1105	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]NHAI,RAJASTHAN , G	10/2014	264.72 -	264.72	-	04/2017 -	-	-	0/0
1106	PHALODI - JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI,RAJASTHAN , G	09/2015	567.51 -	567.51	-	03/2018 -	03/2018	0(O) -	0/0
1107	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN , G	01/1991	269.26 -	269.26	212.72	10/2016 -	10/2016	-	0/0
1108	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAUJI - [N24000406]MORTH,RAJASTHAN , ITEM RATE	01/1991	208.87 223.00	208.87	206.78	05/2016 -	05/2016	-	0/0
1109	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN , G	10/2015	597.00 -	597.00	-	10/2017 -	04/2018	6(O) -	0/0
1110	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN , PPP (BOT)	11/2012	530.07 -	530.07	-	08/2016 -	-	-	0/0
1111	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN , PPP (BOT)	08/2014	822.90 -	822.90	-	04/2018 -	04/2018	0(O) -	0/0
1112	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	-	10/2013 -	10/2013	-	0/0
1113	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	-	10/2013 -	10/2013	-	0/0
1114	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN , PPP (BOT)	02/2008	1,673.70 -	1,673.70	3,165.42	10/2011 -	12/2017	74(O) -	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1115	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS - DHOLPUR - [N24000520]NHAI,RAJASTHAN , G	08/2015	275.90 -	275.90	-	-	02/2018	-	0/0
1116	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI,RAJASTHAN , PPP (BOT)	06/2016	637.18 -	637.18	-	06/2019	06/2019	0(O)	0/0
1117	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN , PPP (BOT)	06/2016	763.23 -	763.23	-	06/2019	06/2019	0(O)	0/0
1118	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589]NHAI,RAJASTHAN , G	06/2016	649.00 -	649.00	-	06/2019	06/2019	0(O)	0/0
1119	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN , G	07/2016	688.70 -	688.70	-	-	-	-	0/0
1120	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN , G	07/2016	331.46 -	331.46	-	-	10/2018	-	0/0
1121	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN , G	08/2016	320.30 -	320.30	-	-	01/2019	-	0/0
1122	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN , G	09/2016	1,239.82 -	1,239.82	-	-	-	-	0/0
1123	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN , G	09/2016	1,100.19 -	1,100.19	-	-	-	-	0/0
1124	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN , G	12/2016	1,031.95 -	1,031.95	-	-	-	-	0/0
1125	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN , G	04/2017	894.00 -	894.00	-	04/2020	04/2020	0(O)	0/0
1126	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN , Central Sector Projects	10/2017	964.17 -	964.17	-	10/2017	10/2017	0(O)	0/0
1127	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM , G	04/2013	151.59 -	151.59	-	08/2013	-	-	0/0
1128	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM , ITEM RATE	04/2013	166.27 -	166.27	-	08/2013	-	-	0/0
1129	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM , ITEM RATE	01/2013	182.28 -	182.00	24.36	02/2013	-	-	0/0
1130	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM , Central Sector Projects	04/2017	388.00 -	447.37	-	10/2017	10/2017	0(O)	0/0
1131	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU , PPP (BOT)	09/2010	852.00 -	852.00	912.18	03/2013	06/2017	-	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1132	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU , PPP (BOT)	09/2011	1,250.00 -	1,250.00	1,329.10	12/2013 -	12/2017	48(O) -	0/0
1133	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU , G	06/2011	600.00 -	600.00	319.76	06/2013 -	-	-	0/0
1134	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU , PPP (ANNUITY)	05/2010	374.00 -	374.00	237.00	05/2013 -	12/2017	55(O) -	0/0
1135	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU , PPP (ANNUITY)	09/2011	485.00 -	485.00	406.68	08/2013 -	12/2017	52(O) -	0/0
1136	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHTH 170 KM) - [N24000213]NHAI,TAMIL NADU , PPP (ANNUITY)	04/2012	624.00 -	624.00	350.79	04/2014 -	-	-	0/0
1137	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU , EPC	03/2015	258.97 268.92	268.92	-	08/2015 -	-	-	0/0
1138	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU , EPC	03/2015	157.18 162.00	162.00	-	07/2015 -	-	-	0/0
1139	CONSTRUCTION OF PAVED SHOULDERS INCULGING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - - [N24000318]MORTH,TAMIL NADU , EPC	11/2015	154.14 -	154.14	-	08/2015 -	08/2015	-	0/0
1140	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU , G	05/2015	1,387.11 -	1,387.11	682.41	11/2017 -	11/2017	0(O) -	0/0
1141	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU , G	06/2015	563.92 -	563.92	95.89	12/2017 -	06/2018	6(O) -	0/0
1142	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU , G	07/2014	401.11 -	401.11	273.89	01/2017 -	-	-	0/0
1143	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU , G	11/2014	563.92 -	563.92	186.50	11/2016 -	06/2018	19(O) -	0/0
1144	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU , PPP (BOT)	03/2007	516.00 -	516.00	761.19	07/2008 -	-	-	0/0
1145	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU , G	02/2016	707.82 -	707.82	129.75	-	08/2018	-	0/0
1146	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU , G	02/2016	641.17 -	641.17	-	-	07/2018	-	0/0
1147	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DSIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU , G	03/2017	848.45 -	848.45	-	03/2020 -	-	-	0/0
1148	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU , Central Sector Projects	03/2016	641.17 -	641.17	64.90	07/2016 -	07/2018	24(O) -	0/0
1149	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU , Central Sector Projects	08/2017	1,176.37 -	1,176.37	-	08/2017 -	08/2017	-	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1150	TWO LANE WITH PS OF KARAUKUDI-RAMANATHPURAM - [N24000698]NHAI,TAMIL NADU , Central Sector Projects	08/2017	652.55 -	652.55	-	08/2017 -	08/2017	-	0/0
1151	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU , Central Sector Projects	09/2017	244.27 -	244.27	-	09/2017 -	09/2017	-	0/0
1152	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU , Central Sector Projects	09/2017	1,227.87 -	1,227.87	-	09/2017 -	09/2017	-	0/0
1153	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA , PPP (BOT)	04/2014	1,266.60 -	1,266.60	-	09/2016 -	03/2018	18(O) -	0/0
1154	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]PWD,TELANGANA , EPC	12/2013	177.18 -	177.18	40.51	03/2016 -	-	-	3/4
1155	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPPLY SECTIO - [N24000242]PWD,TELANGANA , EPC	12/2013	158.65 -	158.65	103.50	03/2016 -	-	-	3/4
1156	YAN TO NIRMAL SEREHALITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA , EPC	12/2013	244.08 -	244.08	38.32	03/2016 -	-	-	1/4
1157	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD,TELANGANA , EPC	01/2014	340.00 -	340.00	-	03/2016 -	-	-	0/2
1158	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]PWD,TELANGANA , EPC	01/2014	270.00 -	270.00	19.84	03/2016 -	-	-	1/4
1159	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]PWD,TELANGANA , EPC	10/2014	244.30 -	156.09	-	12/2016 -	12/2016	-	0/4
1160	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD,TELANGANA , EPC	10/2014	295.47 -	313.27	-	02/2017 -	02/2017	-	0/1
1161	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA , EPC	03/2015	153.21 -	153.21	-	01/2017 -	01/2017	-	0/0
1162	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD,TELANGANA , G	03/2011	218.31 -	339.82	208.28	12/2015 -	-	-	0/3
1163	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA , G	12/2015	1,423.96 -	1,423.96	454.64	- -	11/2018	- -	0/0
1164	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA , EPC	10/2014	369.00 -	369.00	36.90	03/2018 -	03/2018	0(O) -	0/4
1165	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329]NHIDCL,TRIPURA , EPC	05/2014	497.89 -	497.89	70.47	04/2017 -	04/2017	-	0/4

Detail of ongoing Projects Costing Rs150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1166	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH , PPP (BOT)	04/2010	1,267.00 -	1,267.00	2,664.02	06/2013 -	09/2017	-	0/0
1167	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH , PPP (BOT)	02/2011	1,141.00 -	1,141.00	1,986.56	08/2013 -	08/2017	-	0/0
1168	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH , PPP (BOT)	03/2011	1,046.00 -	1,046.00	577.00	09/2013 -	10/2017	49(O) -	0/0
1169	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH , PPP (BOT)	07/2012	291.36 -	291.36	320.46	01/2014 -	12/2017	47(O) -	0/0
1170	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH , PPP (BOT)	03/2013	1,573.00 -	1,573.00	1,850.00	09/2015 -	10/2017	25(O) -	0/0
1171	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH , EPC	03/2015	629.74 -	629.74	-	-	-	-	0/0
1172	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH , EPC	01/2014	282.41 -	282.41	-	03/2016 -	03/2016	-	0/0
1173	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH , EPC	10/2014	227.74 -	227.74	-	10/2016 -	10/2016	-	0/0
1174	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH , G	05/2015	261.09 -	261.09	58.72	05/2017 -	06/2018	13(O) -	0/0
1175	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH , G	04/2014	351.34 -	351.34	391.33	01/2016 -	11/2017	22(O) -	0/0
1176	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH , G	09/2015	368.73 -	368.73	203.84	09/2016 -	09/2017	-	0/0
1177	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH , G	06/2014	301.04 -	301.04	147.92	01/2016 -	-	-	0/0
1178	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI,UTTAR PRADESH , G	04/2014	495.78 -	495.78	522.62	01/2016 -	11/2017	22(O) -	0/0
1179	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH , EPC	10/2013	445.89 -	445.89	-	03/2017 -	03/2017	-	0/0
1180	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]PWD,UTTAR PRADESH , ITEM RATE	11/2010	305.49 -	305.49	-	03/2017 -	03/2017	-	0/0
1181	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH , EPC	01/2014	397.04 -	397.04	-	10/2016 -	10/2016	-	0/0
1182	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP,UTTAR PRADESH , EPC	06/2015	774.57 -	774.57	-	03/2018 -	03/2018	0(O) -	0/0
1183	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH , EPC	10/2013	317.76 -	317.76	15.47	03/2017 -	03/2017	-	0/0
1184	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH , EPC	10/2013	283.45 -	283.45	-	10/2016 -	10/2016	-	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1185	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH , EPC	10/2013	493.94 -	493.94	-	03/2017 -	03/2017	-	0/0
1186	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]NHAI,UTTAR PRADESH , G	09/2015	768.56 -	768.56	530.45	03/2018 -	03/2018	0(O) -	0/0
1187	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436]NHAI,UTTAR PRADESH , G	09/2015	664.53 -	664.53	390.38	03/2018 -	03/2018	0(O) -	0/0
1188	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]NHAI,UTTAR PRADESH , G	09/2015	789.31 -	789.31	603.92	03/2018 -	03/2018	0(O) -	0/0
1189	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH , G	09/2015	785.78 -	785.78	631.26	03/2018 -	03/2018	0(O) -	0/0
1190	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH , PPP (BOT)	07/2015	1,657.20 -	1,657.20	275.00	- -	01/2019	- -	0/0
1191	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH , G	12/2015	611.65 -	611.65	253.48	06/2016 -	06/2018	24(O) -	0/0
1192	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH , G	01/2016	815.28 -	815.28	99.71	06/2018 -	06/2018	0(O) -	0/0
1193	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH , G	01/2016	1,027.53 -	1,027.53	163.91	06/2018 -	06/2018	0(O) -	0/0
1194	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH , G	06/2016	667.00 -	667.00	122.01	07/2018 -	06/2018	-1(O) -	0/0
1195	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH , G	12/2015	667.00 -	667.00	178.32	06/2018 -	06/2018	0(O) -	0/0
1196	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH , EPC	05/2013	164.54 -	164.54	-	08/2015 -	08/2015	-	0/0
1197	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH , EPC	12/2014	207.88 -	207.88	-	- -	-	-	0/0
1198	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH , EPC	12/2014	207.88 -	207.88	-	- -	-	-	0/0
1199	MEERUT-BULANDSHAHAH - [N24000539]NHAI,UTTAR PRADESH , G	01/2016	683.24 -	683.24	.45	- -	-	-	0/0
1200	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]NHAI,UTTAR PRADESH , G	01/2016	701.12 -	701.12	-	- -	05/2019	- -	0/0
1201	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH , G	01/2016	1,081.57 -	1,081.57	-	- -	06/2019	- -	0/0
1202	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH , G	03/2016	676.73 -	676.73	71.78	- -	04/2019	- -	0/0
1203	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH , G	03/2016	1,404.50 -	1,404.50	2.22	- -	-	-	0/0
1204	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPU - [N24000549]NHAI,UTTAR PRADESH , G	03/2016	1,396.74 -	1,396.74	-	- -	-	-	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1205	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH , G	03/2016	1,587.49 -	1,587.49	-	-	04/2019	-	0/0
1206	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH , G	03/2016	899.00 -	899.00	-	-	04/2019	-	0/0
1207	4-LANING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH , G	03/2016	1,668.00 -	1,668.00	-	-	-	-	0/0
1208	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH , G	03/2016	1,408.00 -	1,408.00	-	-	-	-	0/0
1209	4-LANNING OF NAGINA-KSHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH , G	03/2016	1,737.00 -	1,737.00	-	-	-	-	0/0
1210	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH , G	08/2016	2,016.00 -	2,016.00	-	-	04/2019	-	0/0
1211	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH , G	12/2016	534.55 -	534.55	14.95	-	-	-	0/0
1212	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH , G	01/2017	450.68 -	450.68	10.52	-	-	-	0/0
1213	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH , G	03/2017	1,373.28 -	1,373.28	-	03/2020	03/2020	0(O)	0/0
1214	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH , G	03/2017	1,184.71 -	1,310.00	-	03/2020	03/2020	0(O)	0/0
1215	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH , G	03/2017	1,989.00 -	1,989.00	-	03/2020	03/2020	0(O)	0/0
1216	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH , G	03/2017	2,064.99 -	2,447.00	-	03/2020	03/2020	0(O)	0/0
1217	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND , G	11/2011	478.51 -	478.00	409.17	10/2013	12/2017	50(O)	0/0
1218	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND , G	03/2016	720.00 -	720.00	-	-	-	-	0/0
1219	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND , G	03/2016	1,443.00 -	1,443.00	-	-	-	-	0/0
1220	4 LANING OF KSHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND , G	11/2012	605.84 -	605.84	566.25	-	07/2018	-	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1221	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL , PPP (BOT)	02/2011	1,078.84 -	1,078.84	2,400.66	08/2013 -	12/2017	52(O) -	0/0
1222	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL , PPP (BOT)	02/2011	998.79 -	998.79	1,940.09	08/2013 -	03/2018	55(O) -	0/0
1223	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL , PPP (BOT)	04/2012	1,396.18 -	1,396.18	2,710.14	09/2014 -	12/2017	39(O) -	0/0
1224	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL , PPP (ANNUITY)	02/2012	702.16 -	702.16	518.12	07/2014 -	03/2018	44(O) -	0/0
1225	BARSAT-KRISHNANAGAR - [N24000229]NHAI, WEST BENGAL , PPP (ANNUITY)	08/2012	867.00 -	867.00	278.17	02/2015 -	12/2017	34(O) -	0/0
1226	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH, WEST BENGAL , G	01/1991	322.00 -	322.00	56.41	03/2018 -	03/2018	0(O) -	0/0
1227	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL , G	10/2015	361.15 -	361.15	-	- -	01/2018	- -	0/0
1228	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL , G	12/2015	1,083.00 -	1,083.00	139.98	06/2018 -	06/2018	0(O) -	0/0
1229	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL , PPP (BOT)	04/2014	1,665.00 -	1,665.00	2,103.52	- -	12/2017	- -	0/0
1230	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI, WEST BENGAL , G	03/2016	229.37 -	229.37	33.96	- -	11/2018	- -	0/0
1231	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL , G	09/2016	767.03 -	767.03	66.80	- -	08/2018	- -	0/0
	Total		3,27,076.22 -	3,33,448.42	83,379.52				23/182
	<u>SHIPPING AND PORTS</u>								
1232	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL, KERALA , G	03/2007	245.67 -	409.83	350.68	04/2009 -	-	-	0/0
1233	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU, MAHARASHTRA , PPP (BOT)	01/2007	366.39 -	669.46	411.12	12/2010 -	12/2018	96(O) -	0/0
1234	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST, TAMIL NADU , Public Private (SPV)	06/2005	2,427.40 -	2,427.40	831.21	10/2008 -	-	-	0/0
1235	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST, TAMIL NADU , Public Private (SPV)	10/2002	150.00 -	600.00	139.80	03/2006 -	12/2017	141(O) -	0/0
1236	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065]KPL, TAMIL NADU , PPP (ANNUITY)	10/2013	198.94 -	235.15	98.60	06/2017 -	-	-	0/1
1237	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]KPL, TAMIL NADU , PPP (ANNUITY)	02/2015	244.50 258.00	258.33	.14	12/2017 -	12/2017	0(O) -	0/1
1238	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED - [N25000067]KPL, TAMIL NADU , G	12/2014	274.85 -	274.85	43.83	04/2017 -	-	-	0/1

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1239	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068]KPL,TAMIL NADU , G	09/2015	210.00 -	210.00	-	01/2018 -	01/2018	0(O) -	0/0
	Total		4,117.75 -	5,085.02	1,875.38				0/3
	<u>TELECOMMUNICATIONS</u>								
1240	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI , G	06/2016	418.26 -	418.26	-	06/2017 -	-	-	0/0
1241	GUJARAT ACCESS (LOT 1) - [N26000111]BSNL,GUJARAT , Central Sector Projects	09/2017	171.54 -	171.54	-	04/2018 -	04/2018	0(O) -	0/0
1242	MAHARASHTRA NODAL (LOT 1) - [N26000107]BSNL,MAHARASHTRA , Central Sector Projects	08/2017	156.00 -	156.00	-	04/2018 -	04/2018	0(O) -	0/0
1243	MAHARASHTRA CORE (LOT1) - [N26000108]BSNL,MAHARASHTRA , Central Sector Projects	08/2017	156.77 -	156.77	-	04/2018 -	04/2018	0(O) -	0/0
1244	MAHARASHTRA ACESS (LOT 1) - [N26000109]BSNL,MAHARASHTRA , Central Sector Projects	08/2017	213.00 -	213.00	-	05/2018 -	05/2018	0(O) -	0/0
1245	MADHYA PRADESH ACCESS (LOT1) - [N26000110]BSNL,MAHARASHTRA , Central Sector Projects	08/2017	215.30 -	215.30	-	05/2018 -	05/2018	0(O) -	0/0
1246	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE , G	03/2012	13,334.00 -	24,664.00	6,660.00	07/2015 -	06/2019	47(O) -	0/0
1247	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI,MULTI STATE , Central Sector Projects	09/2014	2,111.17 -	2,011.17	253.90	09/2014 -	-	-	0/70
	Total		16,776.04 -	28,006.04	6,913.90				0/70
	<u>URBAN DEVELOPMENT</u>								
1248	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH , G	06/2014	157.84 -	157.84	101.16	03/2017 -	-	-	0/5
1249	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH , G	08/2007	246.90 -	246.90	-	- -	-	-	0/0
1250	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR , G	02/2016	496.18 496.00	496.18	-	06/2017 -	-	-	0/0
1251	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI , G	09/2011	38,585.00 -	38,585.00	30,035.84	03/2016 -	12/2016	-	0/0
1252	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI , G	10/2013	1,219.21 2,230.23	1,592.00	136.13	10/2019 -	03/2020	5(O) -	0/0
1253	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI , G	07/2012	884.30 -	884.30	503.45	12/2015 12/2017	03/2018	27(O) 3(R)	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1254	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC, DELHI , G	06/2012	4,264.00 -	4,118.00	2,841.57	11/2019 -	11/2019	0(O) -	1/7
1255	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD, DELHI , G	06/2015	197.33 -	197.33	4.05	- -	04/2019	- -	0/2
1256	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD, HIMACHAL PRADESH , G	11/2012	270.83 -	270.83	118.14	11/2014 -	10/2018	47(O) -	0/0
1257	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD, JHARKHAND , G	09/2012	171.86 -	171.86	38.63	03/2016 -	12/2018	33(O) -	1/6
1258	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL, KARNATAKA , G	02/2014	26,405.14 -	26,405.14	2,391.46	02/2019 -	03/2020	13(O) -	0/0
1259	RESIDENTIAL QUARTERS FOR HAL, BANGLORE - [N28000103]CPWD, KARNATAKA , G	12/2016	246.31 -	246.31	-	02/2020 -	02/2020	0(O) -	0/0
1260	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD, KERALA , G	01/2010	165.23 -	165.23	25.91	10/2012 04/2017	03/2018	65(O) 11(R)	0/1
1261	KOCHI METRO RAIL PROJECT - [N28000081]KMRL, KERALA , G	07/2012	5,181.79 -	5,181.79	-	07/2017 -	12/2019	29(O) -	0/0
1262	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER - [N28000093]CPWD, KERALA , G	07/2015	154.00 -	154.00	71.90	11/2015 -	12/2017	25(O) -	0/0
1263	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD, MADHYA PRADESH , G	12/2012	188.87 -	188.87	166.54	12/2015 12/2017	12/2017	24(O) 0(R)	0/0
1264	CONSTRUCTION OF 1003 NOS 900 NOS TYPE 2 AND 54 NOS TYPE3 AND 33 NOS TYPE 4 AND 16 NOS TYPE 5 FAMILY - [N28000095]CPWD, MADHYA PRADESH , EPC	12/2016	164.00 -	164.00	69.24	01/2018 05/2018	05/2018	4(O) 0(R)	5/11
1265	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD, MAHARASHTRA , G	02/2011	241.33 349.33	349.33	252.50	03/2016 12/2017	03/2018	24(O) 3(R)	0/13
1266	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD, MAHARASHTRA , G	06/2010	205.00 166.97	170.62	146.41	03/2012 -	03/2018	72(O) -	11/20
1267	NAGPUR METRO RAIL - [N28000085]NMRL, MAHARASHTRA , G	08/2014	8,680.00 -	8,680.00	1,688.81	03/2018 -	12/2019	21(O) -	0/0
1268	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRL, MAHARASHTRA , G	07/2013	23,136.00 -	23,136.00	-	01/2015 -	-	-	0/0
1269	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD, MANIPUR , Central Sector Projects	02/2014	216.69 -	216.69	52.00	03/2015 -	11/2018	44(O) -	0/10
1270	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD, PUNJAB , G	02/2014	388.00 -	388.00	289.64	05/2017 02/2018	02/2018	9(O) 0(R)	7/12
1271	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]CPWD, PUNJAB , G	08/2016	294.00 -	294.00	43.83	04/2019 -	04/2019	0(O) -	0/8
1272	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN - [N28000091]CPWD, RAJASTHAN , Central Sector Projects	08/2014	350.02 479.87	479.87	388.94	03/2015 12/2017	12/2017	33(O) 0(R)	0/0
1273	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD, TAMIL NADU , G	04/2014	332.72 -	332.72	260.88	09/2016 -	11/2017	14(O) -	0/0

Detail of ongoing Projects Costing Rs150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(October 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1274	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU , G	02/2009	14,600.00 19,058.00	19,058.00	14,784.59	12/2015 -	12/2017	24(O) -	11/24
1275	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT - [N28000089]CPWD,TAMIL NADU , G	12/2015	209.00 -	209.00	10.50	- -	-	-	0/6
1276	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU , G	06/2016	3,770.00 -	3,770.00	-	03/2018 -	03/2018	0(O) -	0/0
1277	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA , G	10/2016	209.84 -	209.84	.46	03/2020 -	03/2020	0(O) -	0/5
1278	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH , G	01/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 -	03/2019	0(O) -	0/0
1279	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND , G	12/2008	114.26 266.00	266.00	-	12/2013 -	10/2019	70(O) -	0/0
1280	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL , G	02/2014	156.57 -	156.57	119.37	08/2016 -	03/2018	19(O) -	8/13
1281	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL , Central Sector Projects	10/2014	162.88 -	162.88	30.74	04/2018 -	06/2019	14(O) -	0/0
	Total		1,38,993.10 -	1,44,033.10	57,109.46				44/143
	DEFENCE PRODUCTION								
1282	CONSTRUCTION WORKS PHASE 4 - [N39000001]GSL,GOA , G	12/2016	167.69 168.00	172.99	24.16	05/2018 -	05/2018	0(O) -	3/5
1283	CONSTRUCTION WORKS PHASE 3B - [N39000002]GSL,GOA , G	12/2016	285.95 286.00	296.05	31.52	08/2020 -	08/2020	0(O) -	1/3
	Total		453.64 -	469.04	55.68				4/8
	Grand Total		15,58,352.33	17,59,443.87	6,59,009.46				2000/3883

ANNEXURES
OF PROJECTS HAVING COST
Rs 150 CRORE AND ABOVE

Annexure - I

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE (OCTOBER 2017)

(All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	ANDAMAN & NICOBAR ISLANDS	1	314.61	441.33	26.44
2	ANDHRA PRADESH	59	97,031.51	1,01,034.54	13,586.45
3	ARUNACHAL PRADESH	31	16,602.41	33,555.84	17,329.95
4	ASSAM	48	33,455.72	49,152.55	32,629.54
5	BIHAR	78	65,774.22	82,592.48	38,571.25
6	CHHATISGARH	38	82,769.79	84,975.67	48,906.32
7	D & N HAVELI	1	6,086.08	5,479.75	2,148.82
8	DELHI	16	50,520.06	50,799.67	35,176.89
9	GOA	9	4,043.51	4,058.91	136.89
10	GUJARAT	44	39,186.12	41,822.49	18,130.11
11	HARYANA	21	14,081.22	15,967.45	11,172.71
12	HIMACHAL PRADESH	12	14,659.32	22,591.6	8,911.14
13	JAMMU AND KASHMIR	10	27,408.66	55,639.93	22,962.66
14	JHARKHAND	48	46,724.53	50,436.69	20,329.68
15	KARNATAKA	44	72,280.39	81,988.83	24,826.07
16	KERALA	21	21,774.25	27,871.82	2,619.45
17	MADHYA PRADESH	57	59,615.97	64,062.26	18,419.3
18	MAHARASHTRA	120	1,73,108.23	1,83,029.42	60,256.28
19	MANIPUR	2	944.25	9,874.69	5,516.91
20	MEGHALAYA	6	7,108.02	9,025	273.16
21	MIZORAM	5	2,001.2	6,942.57	3,169.59
22	MULTI STATE	182	2,99,488.52	2,97,634.29	92,365.23
23	NAGALAND	7	8,126.79	10,276.79	368.41
24	ODISHA	68	72,862.34	80,530.99	20,250.59
25	PUNJAB	28	15,555.77	15,561.5	3,448.32
26	RAJASTHAN	62	44,731.54	47,002.58	18,229.46
27	SIKKIM	6	2,537.08	5,585.45	931.23
28	TAMIL NADU	61	67,331.87	82,216.33	45,591.09
29	TELANGANA	35	24,832.84	27,489.74	4,698.16
30	TRIPURA	11	4,400.64	9,067.42	5,663.39
31	UTTAR PRADESH	84	1,09,541.15	1,13,231.41	36,056.41
32	UTTARAKHAND	13	16,833.35	17,673.56	8,379.59
33	WEST BENGAL	55	56,620.37	71,830.32	37,927.97
TOTAL		1,283	15,58,352.33	17,59,443.87	6,59,009.46

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(OCTOBER 2017)

CIVIL AVIATION						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	AAI	01/2009	309.46	-	522.95
COAL						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
2	KULDA OCP (MAHANADI COALFIELDS LTD)	MCL	01/2005	302.96	-	329.1
3	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	259.4	-	296.4
4	BALRAM OCP EXTENSION, MCL 8.00 MTY	MCL	12/2007	172.08	-	191.37
5	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	207.28	-	223.25
HEAVY INDUSTRY						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
6	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	NATIS	04/2011	1718	-	2289
PETROLEUM						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
7	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD	ONGC	04/2012	600.17	-	657
8	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	993	-	1544.61
9	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	871.35	-	958.5
POWER						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
10	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	3919.59	-	6529.67
11	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	6285.33	-	9518.76
12	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	2978.48	-	3321
13	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	3642.04	-	5073.99
14	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	573.99	1337.76	1508.72
15	SYSTEM STRENGTHENING XII OF SR	PGCIL	02/2010	232.34	-	238.62
16	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	297.33	346.79	361.27
17	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	436.68	-	473.75

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(OCTOBER 2017)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
RAILWAYS						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
18	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	NCR	04/1986	158.77	274.56	629.43
19	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	SCR	12/1994	124.43	-	919.06
20	AMRAVATI-NARKHER NL(CR)	CR	06/1994	663.01	668.34	696.87
21	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL	RVNL	04/1995	304	-	328.04
22	CALICUT-MANGALORE (DL) (SR)	SR	02/1996	240	-	537.02
23	MANDARHILL-DUMKA-RAMPURHAT (NL), ER	ER	04/1995	900.05	-	980.99
24	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	514.68	-	812.01
25	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	386.3	-	967.96
26	NANGALDAM-TALWARA(NL), NR	NR	03/1981	450	-	484.14
27	KARUR-SALEM(NL), SR	SR	02/1997	155.55	-	855
28	NANDYAL-YERRAGUNTLA(NL), SCR	SCR	03/1996	155.74	164.36	874.72
29	KANPUR KASGANJ MATHURA(GC) NER	NER	03/1997	677.97	1062.36	1706.54
30	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	1500	-	4837.3
31	MUNEERABAD-MAHABOBNAGAR(NL), SCR	SCR	04/1997	218.24	236.41	544.2
32	RANCHI-LOHARDAGA(GC), SER	SER	04/1997	194.07	-	548.77
33	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	247.66	-	972.82
34	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	501.69	335.77	876.49
35	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	108	-	446.52
36	KATIHAR - JOGBANI (GC)(NEFR)	NFR	09/2001	492.98	-	919.93
37	GULBARGA-BIDAR, SCR(NL)	SCR	02/1998	242.42	369.7	927.68
38	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	NER	04/1999	744.71	744.71	761.7

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(OCTOBER 2017)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
39	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	162.87	-	183.72
40	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	NR	03/2002	625.3	408.76	841.57
41	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	SR	03/1998	280	-	834.61
42	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	NFR	04/2000	733	-	2389.6
43	TOLLYGANJ-GARIA WITH EXTENSION TO DUMDUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	M RTP	03/2000	1049.69	-	3544.3
44	GADWAL - RAICHUR (NL), SCR	SCR	04/1998	92.63	-	316.64
45	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	607.09	-	613.71
46	JIND-SONEPAT (NL),NR	NR	01/2004	238.56	-	722.65
47	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	470.21	-	914.57
48	RAJATGARH-BARANG(LD),ECOR	RVNL	04/1999	166.16	-	369.49
49	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	727.56	-	5464.91
50	MAHARAJGANJ-MASRAKH (NL) - NER	NER	04/2003	218.19	-	356.65
51	ETAWAH-MAINPURI (NL),NCR	NCR	04/1997	120	-	210.67
52	HATHUA-BHATNI (N L) (NER)	NER	04/2005	230.03	-	275.2
53	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	183.23	-	482.09
54	RAICHUR-GUNTAKAL(DL)(SCR)	RVNL	04/2003	136.62	-	1011.85
55	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	332.92	283.95	495.4
56	GOELKERA-MANOHARPUR, (LD)(SER)	RVNL	03/1997	261.7	-	795.83
57	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	743	-	1410.14
58	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	324.9	-	710.67
59	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII' -AGASTIYAMPALLI	SR	09/2007	404.19	-	965.52
60	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	SR	09/2006	343.17	-	1051.14
61	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	NFR	12/2006	170	-	440.72

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(OCTOBER 2017)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
62	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	200	-	427.71
63	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	300	-	921.06
64	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	325	-	618.19
65	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	813.34	-	2365.89
66	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	619.34	-	1749.95
67	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	SWR	04/2007	482	-	989.29
68	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	NWR	04/2008	653.19	-	653.42
69	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR)	NWR	04/2008	516.23	-	694.13
70	TINPAHAR - SAHIBGANJ (ER)	ER	04/2008	167.73	-	207.11
71	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	ER	04/1999	207.52	-	293.47
72	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	603.04	-	628.11
73	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR)	WR	04/2008	1389.62	-	1513.78
74	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	WR	04/2006	117.36	196.95	202.29
75	KATAKHAL TO BHAIRABI	NFR	04/1998	227.9	-	412.4
76	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	1676.31	-	7082.91
77	BHOJIPUR TANAKPUR VIA PILIBHIT	NER	03/2008	195.64	-	405.98
78	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP	NER	03/2012	199.75	-	215.55
79	AHMEDABAD-BOTAD (GC)	RVNL	04/2012	567.18	-	2326.34
80	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	446	-	590.6
81	VIRAMGAM-SURENDRANAGAR (DL)	WR	04/2010	279.4	-	323.64
82	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR	NWR	04/2013	456	-	594.36
83	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	NWR	04/2010	739.65	-	796.25
84	TAMLUK-BASULYA-SUTAHATA DOUBLING	RVNL	04/2010	171.02	-	241.47

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(OCTOBER 2017)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
85	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	309.44	-	402.65
86	SAKRI-HASANPUR ROAD (NL)	ECOR	04/1999	175.69	-	253.1
87	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	SR	04/1998	271.24	-	464.68
88	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	RVNL	04/2008	822.39	-	1652.42
89	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	895	-	1489.68
90	NEW COOCHBEHAR TO SAMUKTALA	NFR	04/2011	209.77	-	393.8
91	CHENGANNUR-CHINGAVANAM	SR	04/2006	191.72	-	360.22
92	ERNAKULAM-KUMBALAM	SR	04/2010	189.24	-	189.35
93	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	NFR	04/1999	523.17	-	1071.96
94	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	312.12	-	495.86
95	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC	ER	04/2010	423.66	-	456.58
96	PEN ROHA DOUBLING	CR	04/2007	98.74	-	312.12
97	PANVEL PEN DOUBLING	CR	04/2006	96.16	-	268.37
98	MUNIRABAD (GINGERA) -RAICHUR NL	SWR	04/2007	179.65	-	782.44
99	JAGGAYYAPET - MELLACHERUVU	SCR	04/2007	313.24	-	342
100	JHARSUGUDA-RENGALI DOUBLING	ECOR	03/2006	201	-	242.28
101	DELANG-PURI DOUBLING	ECOR	03/2011	165.16	-	224.64
102	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM)	RVNL	04/2011	190.1	-	286.57
103	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM)	NER	04/1997	836.26	-	1026.65
104	MUZAFFARPUR-SITAMARHI NEW LINE	ECR	01/1991	332.15	-	538.21
105	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS	NFR	04/2003	4300	-	4422.02
106	RAIPUR - TITLAGARH - DOUBLING	RVNL	03/2007	758.09	-	826.51

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(OCTOBER 2017)

ROAD TRANSPORT AND HIGHWAYS						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
107	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	NHAI	12/2003	280	-	410.8
108	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	199.81	-	214.03
109	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	NHAI	12/2003	167.64	-	276.13
110	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	155.04	-	195.35
111	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	NHAI	12/2003	200	-	250.85
112	NALBARI TO BIJNI (AS-6)	NHAI	12/2003	225	-	314.51
113	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	NHAI	12/2003	160	-	205.46
114	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	196	-	342.62
115	BRAHMPUTRA BRIDGE, NH NO-31	NHAI	12/2003	217.61	-	389.87
116	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM)	NHAI	05/2009	1108	-	3882.53
117	TALEGAON-AMRAVATI	NHAI	11/2009	567	-	1055.94
118	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	NHAI	09/2010	852	-	912.18
119	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM	NHAI	11/2010	1585	-	2284.33
120	MURADABAD-BAREILLY	NHAI	04/2010	1267	-	2664.02
121	PUNE-SATARA (NH-4)	NHAI	10/2010	1724.55	-	2051.04
122	ROHTAK-BAWAL	NHAI	05/2011	650	-	832.39
123	GHAZIABAD-ALIGARH NH-91	NHAI	02/2011	1141	-	1986.56
124	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	NHAI	09/2011	1250	-	1329.1
125	TIRUPATI - TIRUTHANI - CHENNAI	NHAI	04/2011	571	-	622.89
126	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	NHAI	11/2011	1535	-	3123.77
127	PANIKHOLI-RIMOLI	NHAI	03/2012	1410	-	1555.96
128	MUZAFFARNAGAR-HARIDWAR	NHAI	09/2011	754	-	1112.95
129	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	1078.84	-	2400.66

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(OCTOBER 2017)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
130	4-LANING OF BRAHAMPURE-FARAKA	NHAI	02/2011	998.79	-	1940.09
131	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	NHAI	12/2011	1047	-	1629.83
132	6-LANING OF DHANKUNI-KHARAGPUR SECTION	NHAI	04/2012	1396.18	-	2710.14
133	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	NHAI	07/2012	291.36	-	320.46
134	ETAWAH CHAKERI	NHAI	03/2013	1573	-	1850
135	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	1928.22	-	2488
136	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	NHAI	05/2013	1348.2	-	1790.5
137	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232	NHAI	04/2014	351.34	-	391.33
138	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI	NHAI	04/2014	495.78	-	522.62
139	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	NHAI	01/2015	972.5	-	1460.25
140	NAGPUR - KONDHALI	NHAI	09/2005	168	-	279.92
141	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	NHAI	02/2008	1673.7	-	3165.42
142	FOUR LANING OF KAITHAL - RAJASTHAN BORDER	NHAI	07/2015	1393	-	2262.08
143	FOUR LANING OF AURANGABAD - YEDISHI	NHAI	07/2015	1871.34	-	2709.38
144	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS	NHAI	04/2010	1170.52	-	2082.05
145	SIX-LANING OF BARWA ADDA-PANAGARH	NHAI	04/2014	1665	-	2103.52
146	TRICHY - KARUR	NHAI	03/2007	516	-	761.19

SHIPPING AND PORTS

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
147	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	03/2007	245.67	-	350.68
148	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT	01/2007	366.39	-	411.12

STEEL

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
149	EXPANSION OF BHILAI STEEL PLANT	SAIL	08/2010	17265	-	18052.7

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(OCTOBER 2017)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
150	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	HSCL	03/2007	149.73	173	178.65
151	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCL	05/2005	768.88	1070.97	1085.64

Details of Projects Ahead of Schedule w.r.t. Original Schedule

Costing Rs.150 Crore and above						(October 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>PETROLEUM</u>						
1	PARADIP HYDERABAD PIPELINE - [N16000194]	1/2015	2,321.00 -	2,321.00	55.55	12/2020 -	08/2020
2	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]	11/2014	6,068.80 6,068.80	5,296.93	4,250.08	04/2019 03/2019	03/2019
3	GAMJI REDEVELOPMENT PROJECT - [N16000202]	5/2015	1,671.22 567.22	567.22	347.69	11/2019 12/2018	12/2018
	Total		10,061.02 -	8,185.15	4,653.32		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
4	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]	6/2016	667.00 -	667.00	122.01	07/2018 -	06/2018
	Total		667.00 -	667.00	122.01		
	<u>POWER</u>						
5	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) - [N18000207]	1/2016	244.19 -	244.19	116.50	07/2018 -	10/2017
6	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]	1/2016	162.11 -	162.11	115.28	05/2018 -	12/2017
	Total		406.30 -	406.30	231.78		
	<u>PETROLEUM</u>						
7	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216]	1/2016	247.52 -	247.52	53.50	02/2019 -	12/2018
	Total		247.52 -	247.52	53.50		
	<u>RAILWAYS</u>						
8	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]	4/2015	1,172.92 -	1,172.92	74.32	03/2021 -	03/2020
	Total		1,172.92 -	1,172.92	74.32		
	<u>PETROLEUM</u>						
9	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP - [N16000226]	2/2016	356.00 -	356.00	72.34	05/2019 -	12/2018
10	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	658.62 910.23	910.23	5.22	03/2023 03/2022	03/2022
11	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]	5/2016	664.00 -	664.00	147.71	12/2020 -	02/2020

Costing Rs.150 Crore and above						(October 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		1,678.62 -	1,930.23	225.27		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
12	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660	3/2017	296.19 -	254.00	-	03/2020 -	05/2019
	Total		296.19 -	254.00	.00		
	<u>PETROLEUM</u>						
13	MUMBAI REFINERY EXPANSION PROJECT - [N16000281	9/2015	4,199.00 -	4,199.00	194.97	03/2020 -	07/2019
	Total		4,199.00 -	4,199.00	194.97		
	Grand Total		18,728.57	17,062.12	5,555.17		

Details of On Schedule Projects w.r.t. Original Schedule

Annexure - IV

Costing Rs.150 Crore and above						(October 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
1	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]	3/2016	869.44 -	869.44	111.56	03/2021 -	03/2021
2	ADASA UG TO OC - [N06000133]	8/2015	288.90 -	288.90	-	03/2023 -	03/2023
3	MALACHUA OPENCAST PROJECT - [N06000139]	10/2015	488.33 -	488.33	1.06	03/2023 -	03/2023
4	BHATADI EXPANSION OC MINE - [N06000150]	2/2016	304.52 -	304.52	125.81	03/2019 -	03/2019
5	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	369.08	03/2021 -	03/2021
6	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	229.90	03/2025 -	03/2025
7	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	430.95	03/2018 -	03/2018
8	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	34.39	03/2021 -	03/2021
9	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	682.14	03/2026 -	03/2026
10	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	7.61	03/2022 -	03/2022
11	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	7.72	03/2020 -	03/2020
12	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	69.58	03/2020 -	03/2020
13	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	271.12	03/2022 -	03/2022
14	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	174.80	03/2020 -	03/2020
15	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	75.98	03/2026 -	03/2026
16	DHANKASA UG (1.00 MTY) - [N06000155]	9/2016	458.07 -	458.07	-	03/2022 -	03/2022
17	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	1,369.37	03/2023 -	03/2023
18	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	114.37	03/2021 -	03/2021
19	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	47.23	03/2020 -	03/2020
20	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	28.74	03/2022 -	03/2022
21	BHANEAGAON OC - [N06000121]	2/2015	187.94 -	409.68	72.23	03/2023 02/2017	03/2023
22	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(October 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
23	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	175.44	03/2020 -	03/2020
24	GOKUL - [N06000120]	11/2014	267.67 -	267.67	204.35	03/2018 -	03/2018
25	BATURA OCP (2.0 MTY) - [N06000049]	8/2015	1,186.64 -	1,186.64	58.50	03/2023 -	03/2023
26	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]	5/2014	479.15 -	479.15	20.80	03/2019 -	03/2019
27	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	5/2015	397.09 -	442.42	25.07	03/2019 -	03/2019
28	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]	3/2015	522.45 -	522.45	5.65	09/2019 -	09/2019
29	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	362.59	03/2020 -	03/2020
30	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	1,123.80	11/2021 -	11/2021
31	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	0.57	03/2023 -	03/2023
32	KULDA EXPN OC. (5.00 MTY) - [N06000115]	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
33	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	4.57	03/2021 -	03/2021
34	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
35	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	295.56	86.17	03/2019 -	03/2019
36	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]	2/2016	198.68 -	198.68	39.89	03/2019 -	03/2019
37	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]	7/2016	409.87 -	409.87	12.08	03/2022 -	03/2022
38	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]	6/2010	11,816.40 -	11,816.40	2,519.20	03/2023 -	03/2023
39	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	277.65	0.13	03/2021 -	03/2021
40	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	5.73	03/2023 -	03/2023
41	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]	5/2014	337.66 -	337.66	29.74	03/2019 -	03/2019
42	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]	3/2015	513.63 -	513.63	167.04	12/2019 -	12/2019
43	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
44	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	71.98	03/2021 -	03/2021
45	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	38.29	03/2020 -	03/2020
46	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	138.85	03/2021 -	03/2021
47	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]	12/2015	477.65 -	477.65	-	03/2020 -	03/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(October 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
48	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	319.76	0.04	03/2022 -	03/2022
49	AMERA OC RCE - [N06000123]	2/2015	335.97 -	335.97	48.78	03/2018 -	03/2018
	Total		65,371.36 -	65,639.23	9,362.90		
	<u>DEFENCE PRODUCTION</u>						
50	CONSTRUCTION WORKS PHASE 3B - [N39000002]	12/2016	285.95 286.00	296.05	31.52	08/2020 -	08/2020
51	CONSTRUCTION WORKS PHASE 4 - [N39000001]	12/2016	167.69 168.00	172.99	24.16	05/2018 -	05/2018
	Total		453.64 -	469.04	55.68		
	<u>FERTILISERS</u>						
52	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]	2/2016	482.85 -	494.00	400.18	12/2017 -	12/2017
	Total		482.85 -	494.00	400.18		
	<u>HEALTH AND FAMILY WELFARE</u>						
53	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	9/2014	505.58 -	505.58	238.00	03/2018 -	03/2018
54	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA - [N21000014]	7/2016	312.99 -	312.99	128.00	08/2018 -	08/2018
55	CNCI KOLKATA WEST BENGAL - [N21000015]	8/2016	244.00 -	244.00	72.00	09/2018 -	09/2018
56	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	8/2017	272.19 -	272.19	5.45	03/2019 -	03/2019
57	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]	8/2017	355.15 -	355.15	7.10	03/2019 -	03/2019
58	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]	8/2017	274.19 -	274.19	5.48	03/2019 -	03/2019
	Total		1,964.10 -	1,964.10	456.03		
	<u>MINES</u>						
59	UTKAL D AND E COAL BLOCK - [N10000011]	5/2016	534.00 -	534.00	192.54	01/2020 01/2020	01/2020
60	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	5,540.00 -	5,540.00	23.84	04/2021 04/2021	04/2021
	Total		6,074.00 -	6,074.00	216.38		
	<u>PETROLEUM</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(October 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
61	JAIPUR-PANIPAT NAPTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]	2/2015	890.00 -	887.00	223.15	10/2019 -	10/2019
62	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]	4/2016	327.78 -	200.00	15.19	04/2018 -	04/2018
63	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]	7/2015	2,881.40 -	2,881.40	9.98	12/2019 -	12/2019
64	LPG BP PROJECT KHORDHA - [N16000283]	12/2016	161.59 -	161.59	28.80	12/2019 -	12/2019
65	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]	9/2016	208.35 -	208.35	16.93	07/2020 -	07/2020
66	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]	11/2014	195.63 -	187.10	139.30	09/2018 09/2018	09/2018
67	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]	7/2017	268.79 -	268.79	1.21	07/2022 -	07/2022
68	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	2/2015	749.00 -	749.00	504.66	02/2020 -	02/2020
69	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]	2/2017	968.61 -	968.61	-	11/2019 -	11/2019
70	AUGMENTATION OF CTMPL - [N16000286]	12/2016	228.00 -	228.00	-	06/2020 -	06/2020
71	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY - [N16000290]	1/2017	474.15 -	474.15	110.96	05/2019 -	05/2019
72	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]	1/2015	342.00 -	342.00	-	03/2021 -	03/2021
73	DEVELOPMENT OF B-147 FIELD - [N16000292]	2/2017	546.15 -	546.15	-	11/2019 -	11/2019
74	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]	2/2017	511.30 -	511.30	-	11/2019 -	11/2019
75	DIESEL HYDROTREATOR - [N16000207]	7/2015	1,031.37 -	1,031.37	305.91	01/2018 -	01/2018
76	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	864.69	04/2018 04/2018	04/2018
77	SITARGANJ LPG PROJECT - [N16000282]	2/2017	160.10 -	160.10	20.22	02/2020 -	02/2020
78	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	287.49	14.70	04/2022 -	04/2022
79	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]	9/2015	324.00 -	324.00	1.48	06/2020 -	06/2020
80	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]	5/2016	348.00 -	348.00	0.05	01/2021 -	01/2021
81	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]	3/2015	3,957.00 -	3,397.00	1,399.57	12/2018 -	12/2018
82	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]	4/2016	1,021.00 -	1,021.00	6.35	12/2020 -	12/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(October 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
83	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]	2/2011	913.00 -	1,330.00	1,036.41	06/2018 -	06/2018
84	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]	2/2016	2,582.00 -	2,582.00	250.76	11/2019 -	11/2019
85	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]	3/2016	34,012.00 -	34,012.00	253.97	06/2020 06/2020	06/2020
86	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]	7/2014	247.00 -	247.00	-	03/2021 -	03/2021
87	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	1/2015	1,823.00 -	1,823.00	41.75	12/2020 -	12/2020
88	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]	2/2016	3,313.00 -	3,313.00	65.92	02/2020 -	02/2020
89	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	72.56	08/2021 -	08/2021
90	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	3/2017	2,253.00 -	2,253.00	12.88	12/2019 -	12/2019
91	BSVI UPGRADATION - [N16000257]	9/2016	1,810.00 1,810.00	1,810.00	52.96	12/2019 -	12/2019
92	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]	5/2015	224.00 207.00	207.25	42.14	04/2019 -	04/2019
93	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]	4/2017	420.76 -	420.76	-	09/2018 09/2018	09/2018
94	MMPL PIPELINE REROUTING PROJECT - [N16000261]	4/2013	449.58 -	449.58	97.27	12/2019 -	12/2019
95	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR), CACHAR, ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]	6/2016	423.00 -	423.00	91.45	08/2019 -	08/2019
96	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]	5/2016	212.00 -	212.00	0.08	01/2021 -	01/2021
97	ANKLESHWAR BARODA PIPELINE PROJECT - [N16000232]	7/2014	199.95 -	199.95	121.90	03/2018 -	03/2018
98	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT KOCHI REFINERY - [N16000264]	5/2015	337.06 -	337.06	20.75	08/2018 -	08/2018
99	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	5/2016	4,497.00 -	4,497.00	24.07	12/2018 -	12/2018
100	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]	3/2017	3,212.00 -	3,212.00	1.47	12/2020 -	12/2020
101	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]	7/2015	822.66 -	822.66	223.14	11/2018 -	11/2018
102	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	7/2016	249.85 250.00	244.70	-	05/2020 05/2020	05/2020
103	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]	9/2016	407.00 -	407.00	30.61	09/2019 -	09/2019
104	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]	9/2016	1,879.00 -	1,879.00	209.30	06/2020 -	06/2020
105	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,928.00 -	20,928.00	540.49	07/2020 -	07/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(October 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
106	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]	5/2016	406.00 -	406.00	0.50	10/2020 -	10/2020
107	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]	2/2016	151.00 -	151.00	-	09/2019 -	09/2019
108	ENNORE TERMINAL - [N16000224]	8/2014	393.00 -	393.00	211.60	04/2018 -	04/2018
109	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]	5/2016	261.00 -	261.00	0.05	01/2021 -	01/2021
110	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]	3/2017	2,250.00 -	2,250.00	4.87	12/2019 -	12/2019
111	PALAKKAD LPG PLANT - [N16000225]	2/2015	184.00 -	184.00	81.68	12/2017 -	12/2017
112	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	3/2017	1,828.00 -	1,828.00	0.93	12/2020 -	12/2020
113	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	1,162.56	196.84	03/2026 03/2026	03/2026
114	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]	5/2013	711.00 -	711.00	11.12	06/2020 -	06/2020
115	HALDIA LPG IMPORT FACILITY - [N16000223]	3/2015	694.00 -	694.00	197.10	10/2018 -	10/2018
116	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY - [N16000262]	5/2015	193.40 -	193.40	8.55	01/2019 -	01/2019
117	AURAIYA PHULPUR PIPELINE PROJECT - [N16000231]	7/2015	1,427.94 -	1,427.94	434.76	12/2018 -	12/2018
118	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]	10/2015	135.00 171.00	170.70	81.39	03/2019 -	03/2019
119	RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB,HARYANA) - [N16000242]	11/2016	230.00 -	230.00	13.37	02/2019 -	02/2019
120	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]	9/2016	571.66 -	571.66	-	12/2019 -	12/2019
121	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]	5/2016	429.00 -	429.00	39.02	01/2019 -	01/2019
	Total		1,13,259.82 -	1,13,047.81	8,134.81		
	POWER						
122	50 MW SOLAR POWER PROJECT - [N18000251]	9/2017	287.48 -	287.48	28.25	03/2018 -	03/2018
123	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]	2/2017	5,070.13 -	5,070.13	240.02	04/2020 -	04/2020
124	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]	10/2016	408.46 -	408.46	41.84	01/2019 -	01/2019
125	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]	7/2015	2,247.37 -	2,247.37	688.65	07/2018 -	07/2018

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(October 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
126	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]	10/2016	608.24 -	608.24	6.28	04/2019 -	04/2019
127	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]	3/2017	379.95 -	379.95	19.67	12/2019 -	12/2019
128	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]	2/2017	322.30 -	322.30	15.11	02/2019 -	02/2019
129	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]	2/2017	235.53 -	235.53	7.29	06/2019 -	06/2019
130	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]	5/2016	167.01 -	167.01	40.22	11/2018 -	11/2018
131	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION - [N18000237]	10/2016	167.75 -	167.75	1.16	04/2019 -	04/2019
132	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	2,229.09	10/2017 12/2016	10/2017
133	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]	5/2017	445.89 -	445.89	-	02/2019 -	02/2019
134	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]	8/2017	1,931.39 -	1,931.39	6.91	02/2020 -	02/2020
135	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]	5/2017	186.17 -	186.17	7.74	07/2019 -	07/2019
136	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]	5/2017	175.64 -	175.64	4.99	09/2018 -	09/2018
137	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]	12/2015	3,654.00 -	3,654.00	951.00	04/2019 -	04/2019
138	AMELIA COAL MINE - [N18000252]	1/2017	2,104.21 -	2,104.21	40.37	09/2020 -	09/2020
139	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-B - [N18000255]	4/2015	2,225.00 2,225.00	2,225.00	869.00	01/2018 -	01/2018
140	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	3/2017	3,500.00 3,500.00	3,500.00	55.00	07/2020 -	07/2020
141	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V - [N18000256]	2/2015	1,750.00 -	1,750.00	458.00	06/2018 -	06/2018
142	NORTH EASTERN REGION STRENGTHENING SCHEME IV - [N18000216]	5/2016	409.19 -	409.19	55.00	05/2018 -	05/2018
143	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]	8/2016	431.89 -	431.89	0.62	02/2019 -	02/2019
144	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]	11/2016	330.00 -	330.00	185.90	11/2017 -	11/2017
145	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]	1/2016	207.88 -	207.88	90.85	07/2018 -	07/2018
146	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]	1/2015	268.80 -	340.88	161.96	03/2018 -	03/2018

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(October 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
147	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]	3/2017	251.60 -	251.60	-	06/2019 -	06/2019
148	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	1/2016	10,598.98 -	10,598.98	1,043.00	07/2020 -	07/2020
149	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232]	8/2016	177.52 -	177.52	10.95	02/2019 -	02/2019
150	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]	9/2016	562.25 -	562.25	18.56	03/2019 -	03/2019
151	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]	7/2016	1,429.38 -	1,429.38	113.56	01/2019 -	01/2019
152	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]	4/2016	454.11 -	454.11	81.02	04/2018 -	04/2018
153	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]	4/2016	287.99 -	287.99	75.18	06/2018 -	06/2018
154	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]	2/2017	204.12 -	204.12	7.45	09/2019 -	09/2019
155	KHARGONE STTP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	9,870.51	3,537.00	09/2019 -	09/2019
156	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]	4/2016	790.13 -	790.30	289.21	06/2019 -	06/2019
157	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]	5/2016	766.21 -	766.21	59.23	11/2018 -	11/2018
158	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]	3/2017	337.75 -	337.75	-	06/2019 -	06/2019
159	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]	5/2015	780.33 -	780.33	32.82	10/2018 -	10/2018
160	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]	3/2015	197.40 -	197.40	48.84	03/2018 -	03/2018
161	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I - [N18000220]	4/2016	810.48 -	810.48	355.87	12/2018 -	12/2018
162	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]	3/2017	283.72 -	283.72	7.71	11/2019 -	11/2019
163	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]	5/2016	3,519.59 -	3,519.59	446.63	05/2019 -	05/2019
164	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]	7/2016	300.94 -	300.94	32.90	12/2018 -	12/2018
165	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODISHA - [N18000243]	3/2017	162.31 -	162.31	0.62	03/2019 -	03/2019
166	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]	4/2016	844.64 -	844.64	126.12	04/2019 -	04/2019
167	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]	2/2017	195.05 -	195.05	-	02/2020 -	02/2020
168	WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]	7/2016	150.99 -	150.99	29.37	07/2018 -	07/2018

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(October 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
169	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230	7/2016	333.17 -	333.17	148.98	03/2019 -	03/2019
170	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179	12/2014	6,517.36 -	6,517.36	3,477.53	04/2018 -	04/2018
171	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219	5/2016	14,733.37 -	14,733.37	698.45	11/2019 -	11/2019
172	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208	1/2016	1,455.47 -	1,455.47	557.91	07/2018 -	07/2018
	Total		87,767.61 -	88,153.90	17,403.83		
	RAILWAYS						
173	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372	4/2015	524.00 668.00	668.00	-	03/2020 -	03/2020
174	KATNI-BINA 3RD LINE (263 KM) - [N22000415	6/2016	2,478.23 -	2,478.23	-	03/2022 -	03/2022
175	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397	1/1991	763.18 -	1,428.00	482.05	12/2021 -	12/2021
176	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350	12/2015	1,491.47 -	1,491.47	-	12/2020 -	12/2020
177	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413	3/2012	1,183.25 -	1,183.30	729.14	12/2020 -	12/2020
178	KIUL - GAYA DOUBLING PROJECT - [N22000349	12/2015	1,200.20 -	1,200.20	-	12/2020 -	12/2020
179	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425	5/2014	207.00 -	207.00	142.00	03/2018 -	03/2018
180	RAIPUR - TITLAGARH - DOUBLING - [N22000411	3/2007	758.09 -	758.09	826.51	03/2020 -	03/2020
181	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351	12/2015	1,762.94 -	1,762.94	-	12/2020 -	12/2020
182	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422	10/2013	305.00 -	305.00	218.41	03/2019 -	03/2019
183	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427	12/2015	174.00 -	174.00	94.20	03/2019 -	03/2019
184	BONDAMUNDA RANCHI DOUBLING - [N22000396	3/2016	1,724.20 -	1,724.20	126.44	03/2021 -	03/2021
185	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428	10/2013	343.00 -	343.00	240.72	03/2019 -	03/2019
186	RAMNA - SINGRAULI DOUBLING - [N22000417	8/2015	2,436.21 -	2,436.21	79.66	03/2020 -	03/2020
187	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410	3/2006	960.18 -	960.18	609.51	03/2020 -	03/2020
188	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431	8/2016	234.50 -	234.50	0.39	03/2019 -	03/2019
189	JAGDALPUR-KORAPUT DOUBLING - [N22000376	4/2015	1,547.38 -	1,547.38	34.69	03/2021 -	03/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(October 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
190	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]	1/2013	387.70 -	387.70	351.28	03/2018 -	03/2018
191	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,750.00 -	1,295.42	19.80	03/2022 -	03/2022
192	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	9/2016	1,273.00 1,908.00	1,908.00	-	12/2021 -	12/2021
193	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	4/2015	701.61 -	701.61	37.66	03/2021 -	03/2021
194	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	4/2011	927.01 -	977.00	739.55	03/2019 -	03/2019
195	MULTI MODAL LOGISTICS PARK AT SWARUPGANJ - [N22000423]	4/2012	471.82 -	471.82	19.91	03/2019 -	03/2019
196	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	728.10 -	728.10	25.08	12/2024 -	12/2024
197	BINA - KOTA DOUBLING WITH RE - [N22000414]	4/2011	1,485.65 -	1,485.85	686.19	12/2020 -	12/2020
198	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	969.83	82.00	03/2020 -	03/2020
199	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78 -	723.78	0.22	12/2025 -	12/2025
200	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	169.16	03/2021 -	03/2021
201	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	8/2016	582.13 -	582.13	-	03/2020 -	03/2020
202	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]	12/2015	346.32 -	300.00	206.47	03/2019 -	03/2019
203	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	3/2009	1,514.45 -	1,514.45	-	03/2020 -	03/2020
204	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	3/2009	942.95 -	942.95	0.16	03/2019 -	03/2019
205	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	4/1995	524.43 -	939.00	183.99	12/2021 -	12/2021
206	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]	4/2016	5,200.00 -	5,200.00	-	03/2020 -	03/2020
207	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	4/2015	750.55 -	750.56	20.42	12/2024 -	12/2024
208	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	4/2011	4,295.30 -	1,621.60	217.35	12/2026 -	12/2026
209	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]	1/2011	493.17 -	493.17	383.12	03/2018 -	03/2018
210	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]	4/2015	1,765.90 -	1,765.90	32.39	12/2025 -	12/2025
	Total		44,562.91 -	43,296.95	6,758.47		
	ROAD TRANSPORT AND HIGHWAYS						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(October 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
211	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	3/2017	672.89 -	736.01	-	03/2020 -	03/2020
212	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653	3/2017	1,373.28 -	1,373.28	-	03/2020 -	03/2020
213	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322	3/2015	168.39 -	168.39	16.84	11/2018 -	11/2018
214	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305	5/2015	454.89 -	454.89	22.74	05/2018 -	05/2018
215	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319	6/2015	437.39 -	437.39	21.86	06/2018 -	06/2018
216	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379	1/1991	218.63 -	218.63	29.27	10/2017 -	10/2017
217	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523	12/2011	159.39 -	159.39	-	11/2017 -	11/2017
218	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421	3/2015	235.08 -	235.08	47.81	05/2018 -	05/2018
219	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429	12/2015	225.02 -	159.20	-	12/2018 -	12/2018
220	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324	3/2015	194.11 -	194.11	30.54	05/2018 -	05/2018
221	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430	12/2015	223.30 -	223.30	-	06/2018 -	06/2018
222	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409	5/2011	176.22 -	176.22	-	02/2018 -	02/2018
223	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702	10/2017	639.97 -	639.97	-	10/2017 -	10/2017
224	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703	10/2017	964.17 -	964.17	-	10/2017 -	10/2017
225	JUNAGADH BYPASS - [N24000701	10/2017	232.49 -	232.49	-	10/2017 -	10/2017
226	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695	4/2017	388.00 -	447.37	-	10/2017 -	10/2017
227	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475	11/2015	628.45 -	628.45	20.74	03/2018 -	03/2018
228	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411	11/2014	218.31 -	218.31	-	02/2018 -	02/2018
229	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321	6/2016	829.00 -	829.00	59.85	01/2019 -	01/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(October 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
230	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333	12/2015	621.43 -	621.43	-	06/2018 -	06/2018
231	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326	7/2015	197.16 -	197.16	38.50	10/2018 -	10/2018
232	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328	10/2014	369.00 -	369.00	36.90	03/2018 -	03/2018
233	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410	6/2015	641.02 -	641.02	89.88	12/2017 -	12/2017
234	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438	12/2015	289.99 -	289.99	-	12/2018 -	12/2018
235	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323	10/2014	588.95 -	588.95	80.00	11/2018 -	11/2018
236	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327	3/2015	394.00 -	394.00	-	06/2018 -	06/2018
237	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	1/2014	267.16 352.00	352.05	0.02	11/2017 -	11/2017
238	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5 - [N24000320	6/2015	463.49 -	463.49	9.26	06/2018 -	06/2018
239	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478	12/2015	927.54 -	927.54	29.17	06/2018 -	06/2018
240	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325	10/2015	179.82 -	179.82	8.99	01/2019 -	01/2019
241	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376	1/1991	219.40 -	219.40	-	01/2018 -	01/2018
242	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393	6/2015	774.57 -	774.57	-	03/2018 -	03/2018
243	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508	7/2015	1,871.34 -	1,871.34	2,709.38	01/2018 -	01/2018
244	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587	6/2016	763.23 -	763.23	-	06/2019 -	06/2019
245	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586	6/2016	637.18 -	637.18	-	06/2019 -	06/2019
246	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500	1/2016	830.36 -	830.36	-	07/2018 -	07/2018
247	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445	8/2014	822.90 -	822.90	-	04/2018 -	04/2018
248	4-LANNING OF WARDHA- BUTIBORI SECTION (KM 465.500 TO 524.690) - [N24000657	3/2017	1,030.44 -	1,065.51	-	03/2020 -	03/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(October 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
249	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]	3/2017	648.32 -	503.10	-	03/2020 -	03/2020
250	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436]	9/2015	664.53 -	664.53	390.38	03/2018 -	03/2018
251	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]	12/2015	2,136.97 -	2,136.97	-	12/2018 -	12/2018
252	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]	1/1991	322.00 -	322.00	56.41	03/2018 -	03/2018
253	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]	4/2017	894.00 -	894.00	-	04/2020 -	04/2020
254	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]	9/2015	768.56 -	768.56	530.45	03/2018 -	03/2018
255	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]	3/2017	1,288.07 -	1,420.00	-	03/2020 -	03/2020
256	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]	3/2015	226.31 226.00	226.00	-	10/2017 -	10/2017
257	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]	9/2015	788.51 -	788.51	341.55	03/2018 -	03/2018
258	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]	8/2015	538.08 -	538.08	-	02/2018 -	02/2018
259	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	3/2017	744.64 -	982.00	-	03/2020 -	03/2020
260	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY W - [N24000640]	1/2015	326.63 327.00	327.00	-	04/2018 -	04/2018
261	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]	6/2017	2,485.93 -	2,485.93	-	06/2020 -	06/2020
262	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	3/2017	754.54 -	756.27	-	03/2020 -	03/2020
263	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]	3/2017	239.68 -	235.90	-	03/2020 -	03/2020
264	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]	1/1991	229.41 -	229.41	6.65	05/2018 -	05/2018
265	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]	1/2016	815.28 -	815.28	99.71	06/2018 -	06/2018
266	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]	6/2017	1,958.88 -	1,958.88	-	06/2020 -	06/2020
267	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]	3/2017	1,041.62 -	1,187.10	-	03/2020 -	03/2020
268	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]	12/2015	239.23 -	239.23	168.16	12/2017 -	12/2017
269	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O) - [N24000675]	3/2017	993.16 -	1,434.00	-	03/2020 -	03/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(October 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
270	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493	1/2016	1,027.53 -	1,027.53	163.91	06/2018 -	06/2018
271	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448	1/2016	574.28 -	574.28	204.29	07/2018 -	07/2018
272	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463	12/2015	1,083.00 -	1,083.00	139.98	06/2018 -	06/2018
273	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349	5/2015	1,387.11 -	1,387.11	682.41	11/2017 -	11/2017
274	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471	12/2015	2,168.66 -	2,168.66	-	06/2019 -	06/2019
275	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655	3/2017	247.02 -	157.49	-	03/2020 -	03/2020
276	SIX LANING AND STRENGTHENING OF KM 340+000 TO KM 403+400 OF HUBLI-HAVERI SECTION OF NH-48 (OLD NH-4) - [N24000673	3/2017	985.41 -	1,200.00	-	03/2020 -	03/2020
277	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651	2/2017	904.16 -	904.16	-	02/2020 -	02/2020
278	JAISALMER - BARMER - [N24000348	8/2015	482.27 -	482.27	-	02/2018 -	02/2018
279	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663	3/2017	1,989.00 -	1,989.00	-	03/2020 -	03/2020
280	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664	3/2017	639.79 -	552.90	12.08	03/2020 -	03/2020
281	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357	9/2015	567.51 -	567.51	-	03/2018 -	03/2018
282	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	3/2017	1,184.71 -	1,310.00	-	03/2020 -	03/2020
283	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	3/2017	988.34 -	1,043.28	-	03/2020 -	03/2020
284	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589	6/2016	649.00 -	649.00	-	06/2019 -	06/2019
285	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	3/2017	1,098.06 -	1,160.64	-	03/2020 -	03/2020
286	FOUR LANING OF PARWANOO -SOLAN - [N24000479	9/2015	934.46 -	934.46	177.09	03/2018 -	03/2018
287	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450	9/2015	785.78 -	785.78	631.26	03/2018 -	03/2018
288	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347	8/2015	723.54 -	723.54	562.23	02/2018 -	02/2018
289	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	3/2017	831.58 -	1,177.00	-	03/2020 -	03/2020
290	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440	9/2015	789.31 -	789.31	603.92	03/2018 -	03/2018

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(October 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
291	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	3/2017	2,064.99 -	2,447.00	-	03/2020 -	03/2020
292	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669	3/2017	165.50 -	172.16	-	03/2020 -	03/2020
293	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666	3/2017	235.48 -	227.77	-	03/2020 -	03/2020
294	UP/HARYANA BORDER - YAMUNA NAGAR - SAHA- BARWALA - PANCHKULA(PKG - 2) - [N24000358	10/2015	562.34 -	562.34	292.94	04/2018 -	04/2018
295	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499	12/2015	667.00 -	667.00	178.32	06/2018 -	06/2018
296	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641	2/2015	239.91 240.00	240.00	-	10/2017 -	10/2017
	Total		62,408.05 -	64,400.53	8,493.49		
	<u>SHIPPING AND PORTS</u>						
297	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068	9/2015	210.00 -	210.00	-	01/2018 -	01/2018
298	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	2/2015	244.50 258.00	258.33	0.14	12/2017 -	12/2017
	Total		454.50 -	468.33	.14		
	<u>STEEL</u>						
299	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110	12/2007	200.00 -	200.00	131.15	03/2018 -	03/2018
300	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112	4/2013	170.00 -	170.00	88.91	04/2018 -	04/2018
301	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118	11/2016	262.87 -	262.87	37.19	06/2019 -	06/2019
302	ALTERNATE GAS NETWORK AT BSL - [N12000093	3/2015	255.19 -	255.19	168.02	03/2018 -	03/2018
303	CENTRAL DISPATCH YARD - [N12000119	8/2015	320.66 -	320.66	17.71	08/2018 -	08/2018
304	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120	7/2015	465.85 -	465.85	41.38	07/2018 -	07/2018
305	FORGED WHEEL PLANT - [N12000116	4/2014	1,682.85 -	1,682.85	63.22	09/2018 -	09/2018
306	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115	11/2015	818.00 -	818.00	28.13	06/2020 -	06/2020
	Total		4,175.42 -	4,175.42	575.71		
	<u>TELECOMMUNICATIONS</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(October 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
307	MADHYA PRADESH ACCESS (LOT1) - [N26000110]	8/2017	215.30 -	215.30	-	05/2018 -	05/2018
308	MAHARASHTRA ACCESS (LOT 1) - [N26000109]	8/2017	213.00 -	213.00	-	05/2018 -	05/2018
309	MAHARASHTRA CORE (LOT1) - [N26000108]	8/2017	156.77 -	156.77	-	04/2018 -	04/2018
310	GUJARAT ACCESS (LOT 1) - [N26000111]	9/2017	171.54 -	171.54	-	04/2018 -	04/2018
311	MAHARASHTRA NODAL (LOT 1) - [N26000107]	8/2017	156.00 -	156.00	-	04/2018 -	04/2018
	Total		912.61 -	912.61	.00		
	<u>URBAN DEVELOPMENT</u>						
312	RESIDENTIAL QUARTERS FOR HAL, BANGLORE - [N28000103]	12/2016	246.31 -	246.31	-	02/2020 -	02/2020
313	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]	6/2016	3,770.00 -	3,770.00	-	03/2018 -	03/2018
314	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]	10/2016	209.84 -	209.84	0.46	03/2020 -	03/2020
315	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,118.00	2,841.57	11/2019 -	11/2019
316	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]	8/2016	294.00 -	294.00	43.83	04/2019 -	04/2019
317	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]	1/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 -	03/2019
	Total		15,712.15 -	15,566.15	5,422.63		
	Grand Total		4,03,599.02	4,04,662.07	57,280.25		

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Annexure - V

(October 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,000.00	09/2010 -	02/2018	71.82
	Total		3,492.00 -	6,000.00			
	<u>CIVIL AVIATION</u>						
2	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT [N04000050]	01/2009	309.46 -	553.53	01/2011 -	10/2017	78.87
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28
	Total		624.07 -	994.86			
	<u>COAL</u>						
4	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	03/2015 -	03/2020	201.44
5	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 -	486.57	03/2012 -	03/2018	87.58
6	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86
7	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	03/2012 -	03/2019	80.24
8	BHANEGAON OC - [N06000121]	02/2015	187.94 -	409.68	03/2023 -	03/2023	117.98
9	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	03/2019 -	03/2019	11.42
10	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	03/2015 -	03/2020	114.60
11	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]	05/2016	687.28 -	830.45	06/2017 -	10/2017	20.83
12	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80	11/2021 -	11/2021	.00
	Total		19,751.90 -	21,154.17			
	<u>DEFENCE PRODUCTION</u>						
13	CONSTRUCTION WORKS PHASE 4 - [N39000001]	12/2016	167.69 168.00	172.99	05/2018 -	05/2018	3.16

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
14	CONSTRUCTION WORKS PHASE 3B - [N39000002	12/2016	285.95 286.00	296.05	08/2020 -	08/2020	3.53
	Total		453.64 -	469.04			
	<u>FERTILISERS</u>						
15	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009	10/2014	197.79 -	209.44	11/2016 -	04/2019	5.89
16	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010	02/2016	482.85 -	494.00	12/2017 -	12/2017	2.31
	Total		680.64 -	703.44			
	<u>HEALTH AND FAMILY WELFARE</u>						
17	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005	11/2013	196.70 -	209.00	01/2016 -	-	6.25
	Total		196.70 -	209.00			
	<u>HEAVY INDUSTRY</u>						
18	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78
	Total		1,718.00 -	3,827.30			
	<u>PETROLEUM</u>						
19	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167	07/2011	352.56 -	439.03	03/2017 -	11/2018	24.53
20	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169	01/2006	993.00 -	1,693.00	01/2012 -	11/2017	70.49
21	LPG TERMINAL AT KOCHI - [N16000171	10/2015	607.06 -	714.25	10/2017 -	03/2019	17.66
22	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172	05/2013	4,124.35 -	5,637.00	04/2016 -	12/2017	36.68
23	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175	03/2014	3,076.00 -	4,190.00	09/2017 -	06/2018	36.22
24	MH NORTH REDEVELOPMENT PHASE III - [N16000188	06/2014	5,706.47 -	5,813.25	05/2017 -	05/2018	1.87
25	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127	06/2010	202.94 -	330.35	01/2014 -	11/2019	62.78

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
26	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79 -	1,256.72	05/2013 -	12/2017	45.83
27	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	03/2018	29.42
28	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]	02/2011	913.00 -	1,330.00	06/2018 -	06/2018	45.67
29	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	723.40	10/2014 -	03/2018	133.50
30	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	11/2017	37.72
31	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]	11/2011	310.00 -	370.00	03/2013 -	-	19.35
32	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	04/2018 -	04/2018	1.77
33	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	658.62 -	910.23	03/2023 -	03/2022	38.20
34	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]	10/2015	135.00 171.00	170.70	03/2019 -	03/2019	26.44
	Total		24,372.27 -	30,690.77			
	POWER						
35	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	8,398.75	09/2009 -	12/2018	114.28
36	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	18,559.49	09/2010 -	-	195.28
37	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	738.48	09/2010 -	03/2018	54.59
38	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]	10/2008	4,824.12 -	5,071.94	10/2012 -	02/2018	5.14
39	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]	04/2010	4,404.57 -	5,135.01	01/2015 -	03/2018	16.58
40	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	13,762.80	08/2013 -	12/2017	23.65
41	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]	02/2010	2,144.00 -	2,932.88	12/2012 -	02/2018	36.79
42	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	04/2016 -	03/2018	38.61
43	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	02/2014	908.08 -	969.97	06/2016 -	11/2017	6.82
44	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	550.18	11/2016 -	03/2018	5.34

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
45	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]	03/2014	155.57 -	206.42	03/2016 -	12/2017	32.69
46	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	03/2020	29.14
47	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	8,149.00	09/2011 -	03/2018	86.25
48	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]	08/2014	288.49 -	376.09	02/2017 -	03/2018	30.37
49	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	02/2014	196.58 -	225.28	02/2016 -	12/2017	14.60
50	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP - [N18000180]	01/2015	268.80 -	340.88	03/2018 -	03/2018	26.82
51	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03	07/2017 -	12/2018	27.92
52	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]	07/2010	1,272.80 -	1,731.10	11/2012 -	12/2017	36.01
53	SYSTEM STRENGTHENING XII OF SR - [N18000085]	02/2010	232.34 -	245.00	06/2012 -	12/2017	5.45
54	DHUKWAN SMALL HYDRO PROJECT - [N18000189]	05/2011	195.42 -	294.60	02/2014 -	12/2018	50.75
55	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	7,998.00	05/2014 -	02/2019	49.41
56	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	13,731.26	01/2018 -	12/2018	5.91
57	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]	05/2015	436.68 -	602.44	12/2016 -	12/2017	37.96
58	BOKARO THERMAL POWER STATION-A - [N18000199]	08/2006	2,313.00 4,139.00	4,366.64	12/2011 -	02/2017	88.79
59	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]	04/2007	4,122.00 8,781.00	9,142.58	02/2011 -	03/2016	121.80
60	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,179.96	12/2009 06/2016	03/2018	147.51
61	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]	09/2011	1,940.13 -	2,702.65	09/2014 -	12/2017	39.30
62	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	3,939.11	02/2016 -	12/2020	137.73
63	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	06/2014 -	09/2018	31.17
64	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,337.76	08/2013 -	03/2018	133.06
65	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	426.29	08/2014 -	12/2017	43.37

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
66	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116	12/2011	1,746.65 -	2,228.71	08/2014 -	12/2017	27.60
67	KISHANGANGA HEP (3X110 MW) - [N18000031	01/2009	3,642.04 -	5,882.01	01/2016 -	02/2018	61.50
68	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258	05/2005	1,779.29 -	2,187.32	11/2008 -	09/2018	22.93
69	BARH STPP(3X660MW) NTPC - [180100242	02/2005	8,692.97 -	15,095.67	01/2011 -	03/2019	73.65
70	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119	07/1998	368.72 -	1,329.43	07/2006 02/2015	11/2017	260.55
71	TRIPURA GAS BASED POWER PROJECT - [N18000071	07/2009	421.01 -	1,078.31	07/2013 -	-	156.12
72	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128	11/2011	723.63 -	882.13	11/2014 -	12/2017	21.90
73	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143	03/2013	514.20 -	703.10	06/2015 -	03/2018	36.74
74	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI-LEH PROJECT - [N18000215	01/2014	1,788.41 -	2,333.71	09/2017 -	09/2018	30.49
75	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222	04/2016	790.13 -	790.30	06/2019 -	06/2019	.02
76	PAKRI BARWADIH COAL MINING PROJECT - [N18000225	10/2004	4,237.96 4,238.00	4,552.00	10/2017 -	10/2017	7.41
77	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253	03/2015	955.00 -	1,364.00	12/2015 -	03/2018	42.83
	Total		1,04,449.62 -	1,63,178.45			
	<u>RAILWAYS</u>						
78	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007	04/1986	158.77 274.56	634.48	03/1994 -	-	299.62
79	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135	04/1983	36.80 274.41	614.00	- -	-	1,568.48
80	CALICUT-MANGALORE (DL) (SR) - [220100151	02/1996	240.00 -	579.37	- -	-	141.40
81	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	920.00	- -	-	491.45
82	KATI HAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	492.98 -	1,320.00	12/2010 -	-	167.76
83	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	1,542.41	- 05/2009	-	536.26

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
84	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263	03/1998	280.00 -	1,122.00	- -	-	300.71
85	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	330.00 -	2,125.18	- -	03/2021	543.99
86	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT (MTP) - [220100268	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
87	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	350.00	02/2011 -	-	277.85
88	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	1,188.91 -	1,319.33	- 12/2009	03/2019	10.97
89	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	607.09 -	973.33	12/2012 12/2012	-	60.33
90	JIND-SONEPAT (NL),NR - [220100280	01/2004	238.56 -	740.00	03/2012 -	-	210.19
91	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	1,185.64	- 09/2009	03/2019	293.06
92	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314	04/2001	470.92 727.13	2,713.09	- -	03/2021	476.13
93	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316	04/2003	218.19 -	412.05	- -	03/2018	88.85
94	KICHHA-KHATIMA (NL) - NER - [220100317	04/2003	142.45 -	228.40	- -	-	60.34
95	ETAWAH-MAINPURI (NL),NCR - [220100318	04/1997	120.00 -	245.39	12/2008 -	-	104.49
96	HATHUA-BHATNI (N L) (NER) - [220100319	04/2005	230.03 -	718.54	- -	05/2019	212.37
97	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	1,101.16	- -	-	186.92
98	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	1,202.70	02/2015 -	12/2019	556.39
99	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	340.00	03/2009 03/2009	12/2017	154.85
100	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	810.78 -	1,928.07	- -	12/2022	137.80
101	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329	04/2003	136.62 -	376.00	12/2007 03/2010	-	175.22
102	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045	03/1997	261.70 -	388.00	02/2006 -	12/2019	48.26
103	BHOPAL BINA 3D LINE DOUBLING - [N22000077	09/2007	687.20 -	950.00	03/2010 -	03/2018	38.24
104	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU PONDY-AGASTIYAMPALLI - [N22000079	09/2007	404.19 -	2,072.50	- -	-	412.75
105	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080	09/2006	343.17 -	1,065.00	- -	-	210.34

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8
106	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	2,300.00	- -	-	404.39
107	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	-	60.77
108	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	4,600.00	04/2014 -	03/2020	642.73
109	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	332.92 283.95	477.88	03/2012 -	-	43.54
110	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56 -	1,160.47	- -	03/2022	206.55
111	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 -	1,825.00	03/2008 06/2008	03/2020	145.63
112	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	941.04	03/2014 -	06/2019	44.07
113	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,030.29	03/2012 -	-	70.85
114	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) [N22000125]	04/2006	117.36 196.95	203.00	03/2011 -	-	72.97
115	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	509.00	12/2012 -	05/2016	123.34
116	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	499.30 -	3,168.29	- -	03/2023	534.55
117	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70 -	792.89	- -	03/2021	185.52
118	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 -	365.67	- -	-	.14
119	HANSDIHA-GODDA NL - [N22000236]	04/2011	267.09 -	350.78	- -	-	31.33
120	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	493.96 -	681.68	- -	-	38.00
121	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC [N22000245]	04/2010	423.66 -	720.59	03/2017 -	-	70.09
122	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 -	199.12	- -	-	8.18
123	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]	04/2012	297.85 -	540.02	- -	03/2022	81.31
124	PEN ROHA DOUBLING - [N22000254]	04/2007	98.74 -	381.39	- -	-	286.26
125	PANVEL PEN DOUBLING - [N22000255]	04/2006	96.16 -	280.00	- -	-	191.18
126	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26
127	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	-	651.97

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8
128	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97
129	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	04/2012	1,054.35 -	2,200.00	- -	-	108.66
130	GUDUR-DURGARAJAPATNAM - [N22000265]	04/2011	283.54 -	759.41	- -	-	167.83
131	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	197.17	- -	-	25.87
132	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	625.00	- -	-	117.77
133	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	4,500.00	- -	-	329.85
134	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	-	24.09
135	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	-	57.65
136	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	- -	-	47.93
137	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,714.49	- -	-	76.69
138	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29
139	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	792.01	- -	-	134.68
140	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63	- -	-	57.68
141	CHANDIGARH-BADDI NL - [N22000296]	04/2007	328.14 -	1,540.00	- -	-	369.31
142	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	-	14.14
143	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00	- -	-	72.07
144	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	-	12.38
145	MONIGRAM- NIMTITA - [N22000301]	04/2012	250.93 -	259.23	- -	-	3.31
146	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	04/2012	255.64 -	272.20	- -	-	6.48
147	JAGGAYYAPET - MELLACHERUVU - [N22000304]	04/2007	313.24 -	554.70	01/1999 -	-	77.08
148	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	750.00	01/1999 -	-	60.78
149	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	01/1999 -	-	53.96
150	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	514.68 -	2,271.50	- -	-	341.34

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
151	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	1,781.98	03/2004 -	03/2020	259.68
152	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168	04/1995	900.05 -	1,125.89	12/2011 12/2010	03/2020	25.09
153	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201	09/1997	1,500.00 -	5,450.00	04/2008 12/2011	06/2018	263.33
154	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35
155	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240	04/1997	501.69 335.77	1,043.56	03/2012 -	-	108.01
156	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	12/2009 -	-	300.67
157	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257	04/1997	162.87 -	541.00	- -	-	232.17
158	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	3,040.00	12/2008 -	03/2019	314.73
159	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	470.21 -	3,004.90	- -	06/2021	539.05
160	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	9,658.00	03/2011 -	03/2020	1,227.45
161	KOSI BRIDGE (NL), ECR - [220100304	04/2002	322.95 -	341.41	03/2012 -	-	5.72
162	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028	04/2006	495.74 -	732.89	06/2013 -	03/2018	47.84
163	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082	12/2006	170.00 -	465.00	03/2011 -	10/2011	173.53
164	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086	09/2006	200.00 -	780.00	- -	03/2019	290.00
165	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087	09/2006	300.00 -	2,135.00	- -	03/2020	611.67
166	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124	04/2006	850.00 -	3,000.00	03/2015 -	03/2020	252.94
167	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
168	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) [N22000119	04/1999	207.52 -	334.87	12/2012 -	-	61.37
169	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT [N22000127	04/1996	1,676.31 -	7,300.00	03/2009 -	03/2018	335.48
170	AGARTALA SABROOM, NL, NEFR - [N22000099	04/2008	813.34 -	3,451.00	03/2014 -	03/2020	324.30
171	KISHANGANJ JALALGARH, NL, NEFR - [N22000101	04/2008	282.92 -	360.00	- -	-	27.24

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8
172	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	4,084.69	12/2015 -	03/2020	204.95
173	KANPUR KASGANJ MATHURA(GC) NER - [220100197	03/1997	677.97 1,062.36	1,679.13	- -	-	147.67
174	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256	04/1999	744.71 -	1,126.79	- -	-	51.31
175	DAUSA-GANGAPUR CITY(NL),NWR - [220100184	02/1997	410.08 -	780.98	- -	08/2018	90.45
176	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) [N22000114	04/2008	516.23 -	735.00	03/2014 -	-	42.38
177	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
178	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	27,946.00	11/2002 -	12/2018	1,017.84
179	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	625.30 408.76	876.10	06/2007 -	-	40.11
180	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	04/2006	325.00 -	1,581.53	03/2010 -	-	386.62
181	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	1,195.00	12/2012 -	-	293.09
182	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	380.00	02/2009 02/2009	06/2017	128.70
183	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075	09/2006	324.90 -	516.40	03/2010 -	12/2017	58.94
184	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110	04/2010	3,951.98 -	4,259.48	03/2016 -	12/2020	7.78
185	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109	04/2010	2,298.42 -	2,733.86	03/2014 -	-	18.95
186	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192	03/1996	155.74 164.36	966.98	02/2009 -	12/2017	520.89
187	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	525.00	- -	03/2019	140.56
188	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	07/2008 -	-	284.00
189	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,776.81	03/1998 -	12/2019	359.96
190	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	-	160.76
191	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097	03/1984	293.97 -	749.69	06/2005 -	-	155.02
192	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	491.33	06/2004 -	-	153.17
193	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	- -	-	840.53

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
194	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]	04/1997	836.26	1,072.52	-	-	28.25
195	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	04/1996	138.00	1,382.78	-	-	902.01
196	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]	04/2007	482.00	874.57	03/2013	-	81.45
197	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24	321.62	03/2012	03/2019	1.06
198	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	679.27	1,579.27	-	03/2021	132.50
199	JHARSUGUDA-RENGALI DOUBLING - [N22000317]	03/2006	201.00	230.00	-	-	14.43
200	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	826.57	1,160.83	-	03/2020	40.44
201	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81	238.03	-	03/2020	52.77
202	DELANG-PURI DOUBLING - [N22000320]	03/2011	165.16	234.71	03/2015	-	42.11
203	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92	197.73	-	-	8.10
204	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]	04/2011	190.10	350.00	-	03/2019	84.11
205	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77	209.00	12/2016	-	40.49
206	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00	648.00	-	03/2020	8.00
207	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]	04/2008	829.74	1,161.64	03/2015	12/2019	40.00
208	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43	1,010.00	-	-	711.70
209	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	663.01	858.97	06/1999	-	29.56
210	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00	2,815.62	-	01/2018	411.93
211	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00	308.00	-	-	.33
212	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78	268.78	-	08/2017	10.26
213	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]	03/2008	195.64	474.30	-	03/2018	142.44
214	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00	477.31	-	10/2018	61.80
215	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00	644.00	-	-	.16

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
216	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	348.55	- -	03/2019	41.64
217	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	567.18 -	975.62	- -	03/2020	72.01
218	DHASA-JETALSAR (GC) - [N22000141]	04/2012	376.59 -	644.38	- -	12/2020	71.11
219	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]	04/2011	439.88 -	845.68	- -	-	92.25
220	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	399.63	- -	03/2019	24.63
221	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	04/2013	1,266.89 -	1,548.66	- -	12/2020	22.24
222	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	1,037.15	- -	03/2019	132.54
223	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]	04/2010	279.40 -	355.00	- -	-	27.06
224	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	2,562.27	- -	-	23.02
225	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	12/2022	226.98
226	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	276.89	- -	10/2018	16.87
227	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR [N22000152]	04/2013	456.00 -	855.16	- -	05/2018	87.54
228	RATANGARH-SARDARSAHAR (MM OF SADULPUR- BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	-	17.92
229	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	272.99	- -	03/2019	27.93
230	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]	04/2012	288.97 -	369.08	- -	10/2018	27.72
231	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	293.68	- -	03/2019	21.31
232	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR- BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	12/2022	226.23
233	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00	- -	-	62.32
234	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00	- -	-	82.25
235	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
236	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	-	53.44
237	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]	04/2010	171.02 -	250.00	06/2013 -	12/2016	46.18

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
238	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	-	88.40
239	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	12/2017	41.36
240	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 -	549.75	- -	-	32.26
241	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
242	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
243	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	- -	-	338.91
244	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]	04/2008	678.62 -	2,393.23	- -	-	252.66
245	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
246	ATTIPPATTU PUTTUR - [N22000184]	04/2008	446.87 -	527.37	- -	-	18.01
247	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	2,350.00	- -	-	348.88
248	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
249	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC [N22000188]	04/1998	271.24 -	520.00	- -	-	91.71
250	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,810.00	- -	03/2018	120.09
251	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
252	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	380.00	- -	-	71.62
253	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,857.00	03/2007 -	04/2016	107.49
254	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00 -	580.00	- -	07/2019	130.16
255	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77 -	630.00	- -	03/2018	200.33
256	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	450.00	- -	03/2019	58.70
257	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22	- -	-	109.04
258	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	302.90	- -	-	84.23
259	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	342.85	- -	-	78.83

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
260	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02 -	6,000.00	- -	03/2021	46.95
261	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00	- -	-	94.45
262	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	-	63.25
263	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	450.00	- -	03/2020	171.38
264	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	04/1999	523.17 -	1,871.00	- -	03/2018	257.63
265	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12 -	535.00	- -	03/2019	71.41
266	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	398.93	- -	03/2019	62.12
267	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2018	29.06
268	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	1,500.00	- -	-	149.41
269	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 -	260.60	- -	-	51.49
270	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	1,130.13	- -	-	23.38
271	PIRPAINTI-BHAGALPUR - [N22000222]	04/2011	261.38 -	332.14	- -	-	27.07
272	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	630.00 -	1,272.19	- -	03/2022	101.93
273	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]	02/2015	2,326.00 -	2,449.91	- -	03/2023	5.33
274	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	- -	-	10.94
275	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]	02/2016	854.00 -	1,035.16	- -	-	21.21
276	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.67	- -	-	9.32
277	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	04/2015	524.00 668.00	668.00	03/2020 -	03/2020	27.48
278	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	559.91	07/2014 -	-	68.57
279	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS - [N22000386]	04/2003	4,300.00 -	4,520.00	- -	08/2015	5.12
280	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 -	871.00	- -	03/2021	.00
281	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	04/2016	556.31 -	612.00	- -	-	10.01

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
282	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	01/1991	763.18 -	1,428.00	12/2021 -	12/2021	87.11
283	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	04/1995	524.43 -	939.00	12/2021 -	12/2021	79.05
284	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]	02/2015	900.00 -	4,131.90	- -	-	359.10
285	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	750.55 -	750.56	12/2024 -	12/2024	.00
286	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 -	2,373.00	03/2003 -	-	130.97
287	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	977.00	03/2019 -	03/2019	5.39
288	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	03/2012	1,183.25 -	1,183.30	12/2020 -	12/2020	.00
289	BINA - KOTA DOUBLING WITH RE - [N22000414]	04/2011	1,485.65 -	1,485.85	12/2020 -	12/2020	.01
290	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,273.00 1,908.00	1,908.00	12/2021 -	12/2021	49.88
	Total		1,23,103.45 -	2,96,496.70			
	ROAD TRANSPORT AND HIGHWAYS						
291	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	12/2017	28.93
292	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	12/2017	92.75
293	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	03/2018	80.68
294	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	12/2017	68.99
295	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	03/2018	106.50
296	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH- 52) FROM - [N24000292]	11/2014	573.96 605.00	605.00	- -	-	5.41
297	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]	12/2011	156.63 276.00	276.00	02/2012 -	-	76.21
298	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]	03/2015	258.97 -	268.92	08/2015 -	-	3.84
299	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]	03/2015	157.18 162.00	162.00	07/2015 -	-	3.07
300	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	04/2010 -	03/2018	42.25

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
301	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	-	2.29
302	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]	03/2010	1,509.10 -	3,237.87	09/2012 -	12/2017	114.56
303	INDORE-JHABUA-GUJRAT/MP - [N24000136]	10/2010	1,175.00 -	1,206.10	04/2013 -	09/2017	2.65
304	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]	10/2014	295.47 -	313.27	02/2017 -	02/2017	6.02
305	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWES - [N24000249]	03/2011	218.31 -	339.82	12/2015 -	-	55.66
306	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	01/2014	255.75 348.00	348.43	09/2017 -	09/2017	36.24
307	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]	01/2014	267.16 352.00	352.05	11/2017 -	11/2017	31.78
308	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265]	11/2014	297.78 330.00	330.00	02/2017 -	02/2017	10.82
309	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]	12/2009	104.00 -	201.00	09/2010 -	09/2010	93.27
310	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	05/2013	1,055.00 -	1,601.77	11/2015 -	09/2017	51.83
311	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]	03/2014	191.50 192.00	192.00	05/2016 -	06/2017	.26
312	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY W - [N24000640]	01/2015	326.63 327.00	327.00	04/2018 -	04/2018	.11
313	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]	02/2015	239.91 240.00	240.00	10/2017 -	10/2017	.04
314	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]	12/2013	319.80 320.00	320.00	05/2016 -	03/2017	.06
315	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]	08/2013	171.96 172.00	172.00	06/2016 -	03/2017	.02
316	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]	03/2014	162.51 163.00	163.00	05/2016 -	03/2017	.30
317	FOUR LANING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	03/2017	1,184.71 -	1,310.00	03/2020 -	03/2020	10.58
318	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	03/2017	744.64 -	982.00	03/2020 -	03/2020	31.88

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
319	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	03/2017	1,030.44 -	1,065.51	03/2020 -	03/2020	3.40
320	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	03/2017	988.34 -	1,043.28	03/2020 -	03/2020	5.56
321	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]	03/2017	1,059.73 -	1,071.00	03/2017 -	-	1.06
322	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]	03/2017	1,098.06 -	1,160.64	03/2020 -	03/2020	5.70
323	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	03/2017	754.54 -	756.27	03/2020 -	03/2020	.23
324	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	03/2017	672.89 -	736.01	03/2020 -	03/2020	9.38
325	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]	03/2017	1,041.62 -	1,187.10	03/2020 -	03/2020	13.97
326	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]	03/2017	165.50 -	172.16	03/2020 -	03/2020	4.02
327	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]	03/2017	1,288.07 -	1,420.00	03/2020 -	-	10.24
328	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	03/2017	2,064.99 -	2,447.00	03/2020 -	03/2020	18.50
329	SIX LANING AND STRENGTHENING OF KM 340+000 TO KM 403+400 OF HUBLI-HAVERI SECTION OF NH-48 (OLD NH-4) - [N24000673]	03/2017	985.41 -	1,200.00	03/2020 -	03/2020	21.78
330	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]	03/2017	831.58 -	1,177.00	03/2020 -	03/2020	41.54
331	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]	03/2017	993.16 -	1,434.00	03/2020 -	03/2020	44.39
332	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]	12/2016	138.93 155.00	155.00	01/2017 -	01/2020	11.57
333	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]	04/2017	388.00 -	447.37	10/2017 -	10/2017	15.30
	Total		25,598.69 -	32,656.93			
	<u>SHIPPING AND PORTS</u>						
334	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	03/2006 -	12/2017	300.00
335	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065]	10/2013	198.94 -	235.15	06/2017 -	-	18.20

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
336	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]	02/2015	244.50 258.00	258.33	12/2017 -	12/2017	5.66
337	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]	03/2007	245.67 -	409.83	04/2009 -	-	66.82
338	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72
	Total		1,205.50 -	2,172.77			
	<u>STEEL</u>						
339	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]	12/2007	202.61 227.00	227.00	12/2016 -	12/2017	12.04
340	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]	10/2011	175.49 206.71	206.71	12/2016 -	-	17.79
341	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]	05/2005	768.88 1,070.97	1,113.34	02/2014 -	-	44.80
342	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	10/2016 -	03/2018	42.39
343	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	03/2007	149.73 173.00	175.94	12/2015 -	-	17.50
	Total		1,639.71 -	2,211.39			
	<u>TELECOMMUNICATIONS</u>						
344	NETWORK FOR SPECTRUM - [N26000101]	03/2012	13,334.00 -	24,664.00	07/2015 -	06/2019	84.97
	Total		13,334.00 -	24,664.00			
	<u>URBAN DEVELOPMENT</u>						
345	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]	02/2011	241.33 -	349.33	03/2016 -	03/2018	44.75
346	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,592.00	10/2019 -	03/2020	30.58
347	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]	02/2009	14,600.00 -	19,058.00	12/2015 -	12/2017	30.53
348	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN - [N28000091]	08/2014	350.02 -	479.87	03/2015 -	12/2017	37.10

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(October 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
349	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101	12/2008	114.26 266.00	266.00	12/2013 -	10/2019	132.80
	Total		16,524.82 -	21,745.20			
	Grand Total		3,37,145.01	6,07,174.02			

Details of Delayed Projects w.r.t. Original Schedule

Annexure - VI

Costing Rs. 150 Crore and above (October 2017)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI, TAMIL NADU	09/2003	3,492.00 5,677.00	6,000.00	5,499.43	09/2010 09/2016	02/2018	89	71.82	
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 -	11,459.00	10,775.00	12/2015 11/2016	11/2019	47	0	
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 -	12,320.00	8,399.00	12/2016 03/2017	12/2020	48	0	
	Total		27,271.00 -	29,779.00	24,673.43					
	<u>CIVIL AVIATION</u>									
4	CONSTRUCTION OF NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT - [N04000050]AAI, SIKKIM	01/2009	309.46 -	553.53	522.95	01/2011 09/2017	10/2017	81	78.87	long rainy season
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	441.33	26.44	09/2018 -	06/2020	21	40.28	
	Total		624.07 -	994.86	549.39					
	<u>COAL</u>									
6	NEYVELI SOLAR POWER PROJECT 130 MW - [N060000151]NLC, TAMIL NADU	05/2016	687.28 830.45	830.45	705.43	06/2017 -	10/2017	4	20.83	
7	RAJMAHAL OC EXP. - [N06000056]ECL, JHARKHAND	09/2009	153.82 -	153.82	127.71	03/2014 -	12/2017	45	0	Delay/non-issuance of patta/ownership certificate for land/plots allotted
8	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL, ODISHA	01/2005	302.96 -	302.96	329.10	03/2010 -	03/2018	96	0	
9	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL, MADHYA PRADESH	10/2007	259.40 -	486.57	296.40	03/2012 -	03/2018	72	87.58	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(October 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
10	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78 -	209.78	143.08	03/2015 -	03/2018	36	0	forest land diversion
11	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	181.19	159.87	03/2012 -	03/2018	72	0	Forest land diversion
12	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	198.95	03/2014 -	03/2018	48	0	
13	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH	11/2009	198.59 -	198.59	169.49	03/2016 -	03/2018	24	0	
14	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	206.80	03/2013 -	03/2018	60	0	
15	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	341.12	03/2016 -	03/2018	24	0	
16	BAROUD OC EXPANSION (RCE)-3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56 -	258.56	151.14	03/2016 -	03/2018	24	0	
17	RG OC -III EXTENSION (PHASE - II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	83.80	06/2015 -	03/2018	33	0	Diversion of Jallaram vagu
18	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 415.37	415.37	143.67	03/2016 -	03/2018	24	-3.5	Aquisition of non forest land
19	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 -	5,907.11	4,834.48	12/2015 04/2018	04/2018	28	0	
20	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	289.45	152.06	05/2014 -	04/2018	47	0	
21	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	269.82	150.11	04/2014 -	04/2018	48	0	
22	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.10 -	490.10	278.35	03/2017 -	05/2018	14	0	
23	MURADIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	12.08	04/2014 -	10/2018	54	0	
24	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	404.99	03/2013 -	11/2018	68	0	
25	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 448.86	448.86	162.30	03/2012 -	03/2019	84	80.24	Geological disturbances
26	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	191.37	03/2010 -	03/2019	108	0	
27	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	223.25	03/2012 -	03/2019	84	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(October 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
28	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.53 -	479.53	219.23	03/2013 -	03/2019	72	0	
29	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL, JHARKHAND	12/2007	179.87 -	179.87	97.03	03/2012 -	03/2019	84	0	
30	TAPIN OCP (2.5 MTY) - [N06000086]CCL, JHARKHAND	08/2008	264.68 -	264.68	153.27	03/2012 -	03/2019	84	0	
31	KARMA OCP (1.0 MTY) - [N06000088]CCL, JHARKHAND	06/2009	162.46 -	162.46	80.63	03/2014 -	03/2019	60	0	
32	KOYAGUDEM OPENCAST PROJECT - [N06000146]SCCL, TELANGANA	10/2015	426.79 -	426.79	-	03/2018 -	03/2019	12	0	
33	MOONIDIH XV SEAM UG - [N06000098]BCCL, JHARKHAND	08/2011	1,230.27 -	1,230.27	198.90	04/2015 -	04/2019	48	0	
34	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC, TAMIL NADU	04/2013	1,458.17 709.06	709.06	302.65	06/2015 09/2019	09/2019	51	-51.37	
35	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL, CHHATISGARH	09/2008	152.43 459.49	459.49	80.16	03/2015 03/2020	03/2020	60	201.44	
36	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH	07/2008	178.44 -	178.44	5.12	03/2014 -	03/2020	72	0	
37	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL, JHARKHAND	08/2007	163.51 -	163.51	93.28	03/2011 -	03/2020	108	0	
38	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29 164.04	164.04	.34	03/2015 -	03/2020	60	-32.3	Aquisition of Non forest land
39	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL, TELANGANA	07/2011	162.76 349.28	349.28	1.31	03/2015 -	03/2020	60	114.6	Aquisition of Private land
40	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL, TELANGANA	07/2012	417.33 417.33	417.33	59.26	07/2016 -	03/2020	44	0	Aquisition of forest land
41	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL, WEST BENGAL	08/2012	1,055.05 -	1,055.05	317.37	03/2018 -	03/2020	24	0	Rehabilitation of:
42	MAGADH OC 20 MTY (CCL) - [N06000015]CCL, JHARKHAND	08/2008	706.40 -	706.40	116.67	07/2012 03/2017	03/2021	104	0	
43	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL, TELANGANA	07/2011	447.06 -	437.51	259.34	03/2015 -	03/2021	72	-2.14	
44	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL, MULTI STATE	02/2017	328.00 -	328.00	45.31	03/2021 -	06/2022	15	0	
45	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL, TELANGANA	12/2009	418.97 -	489.62	48.58	03/2012 -	03/2023	132	16.86	Aquisition of private land
	Total		20,946.90 -	21,229.31	11,544.00					

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(October 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>FERTILISERS</u>									
46	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79 209.44	209.44	82.72	11/2016 04/2019	04/2019	29	5.89	
	Total		197.79 -	209.44	82.72					
	<u>STEEL</u>									
47	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND	10/2013	245.67 -	245.67	196.21	05/2016 -	11/2017	18	0	
48	3RD CONVERTER AND 4TH CASTER - [N12000088]RINL,ANDHRA PRADESH	07/2011	974.76 -	974.76	586.93	07/2016 -	11/2017	16	0	
49	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	18,052.70	03/2013 -	12/2017	57	0	
50	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	227.00	199.95	12/2016 -	12/2017	12	12.04	
51	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	488.40	227.98	10/2016 -	03/2018	17	42.39	
52	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY- JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 253.92	253.92	193.97	06/2016 -	03/2018	21	0	
53	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND	05/2015	1,154.18 -	1,154.18	477.34	12/2017 -	05/2018	5	0	
54	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	1,034.01	194.21	10/2017 -	07/2018	9	0	
55	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	189.00	-	03/2017 -	08/2018	17	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(October 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
56	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC, CHHATISGARH	01/2010	15,525.00 -	15,525.00	12,854.06	05/2015 10/2018	10/2018	41	0	
57	COKE OVEN BATTERY-5 - [N12000117]RINL, ANDHRA PRADESH	12/2011	2,858.00 -	2,500.00	621.35	12/2017 -	10/2018	10	-12.53	
58	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL, MEGHALAYA	04/2014	151.33 -	151.33	7.15	09/2017 -	12/2018	15	0	
59	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL, JHARKHAND	02/2014	787.29 -	787.29	285.30	12/2016 -	12/2018	24	0	
60	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL, ODISHA	04/2015	3,127.30 -	3,127.30	1,380.44	04/2018 -	02/2019	10	0	
61	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL, BIHAR	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72	0	
	Total		45,067.07 -	44,878.86	35,928.80					
	<u>PETROLEUM</u>									
62	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]IOCL, ODISHA	03/2014	238.50 -	238.50	167.48	03/2017 10/2017	10/2017	7	0	
63	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL, KARNATAKA	01/2006	993.00 -	1,693.00	1,544.61	01/2012 -	11/2017	70	70.49	
64	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL, ASSAM	09/2012	871.35 -	1,200.00	958.50	03/2015 -	11/2017	32	37.72	
65	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT (MOPS) - [N16000128]ONGC, MAHARASHTRA	03/2011	861.79 1,256.72	1,256.72	1,170.49	05/2013 12/2017	12/2017	55	45.83	
66	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC, MULTI STATE	05/2013	4,124.35 4,259.59	5,637.00	3,947.52	04/2016 12/2017	12/2017	20	36.68	
67	RESID UPGRADATION PROJECT - [N16000184]CPCL, TAMIL NADU	03/2013	3,110.36 -	3,110.36	2,863.96	11/2015 -	12/2017	25	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(October 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
68	DHDS REVAMP FOR MEETING BS-IV DIESEL QUALITY - [N16000218]CPCL,TAMIL NADU	02/2016	367.11 -	367.11	225.34	04/2017 -	12/2017	8	0	
69	SONAMURA GGS AND PIPELINE PROJECT (PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A - [N16000246]ONGC,TRIPURA	05/2016	215.38 -	215.38	162.34	06/2017 01/2018	01/2018	7	0	
70	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL,TAMIL NADU	05/2015	257.87 -	257.87	139.96	11/2016 -	02/2018	15	0	
71	FUEL QUALITY UPGRADATION (DHDT/DHDS) PROJECT AT GUJARAT REFINERY - [N16000245]IOCL,GUJARAT	02/2016	931.00 -	931.00	400.75	07/2017 -	02/2018	7	0	
72	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 -	2,665.65	1,650.87	03/2015 03/2018	03/2018	36	29.42	
73	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17 -	600.17	657.00	12/2014 03/2018	03/2018	39	0	
74	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 723.40	723.40	394.90	10/2014 03/2018	03/2018	41	133.5	
75	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM	03/2009	228.64 -	209.19	147.06	12/2016 -	03/2018	15	-8.51	
76	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]ONGC,MADHYA PRADESH	03/2009	181.02 -	173.28	127.44	01/2017 03/2018	03/2018	14	-4.28	
77	NEW 250 TMTA LPG PLANT AT PANAGARH - [N16000222]HPCL,WEST BENGAL	08/2014	190.45 -	190.45	130.15	09/2017 03/2018	03/2018	6	0	
78	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 -	2,592.17	2,040.89	05/2014 05/2018	05/2018	48	0	
79	MH NORTH REDEVELOPMENT PHASE III - [N16000188]ONGC,MAHARASHTRA	06/2014	5,706.47 5,813.25	5,813.25	5,554.21	05/2017 05/2018	05/2018	12	1.87	
80	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC,MAHARASHTRA	02/2015	2,899.93 -	2,098.43	1,237.43	05/2017 05/2018	05/2018	12	-27.64	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(October 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
81	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT	09/2011	202.25 -	160.16	106.98	07/2016 06/2018	06/2018	23	-20.81	
82	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL	03/2014	3,076.00 4,190.00	4,190.00	2,125.22	09/2017 06/2018	06/2018	9	36.22	
83	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 -	2,378.89	2,060.68	03/2013 09/2018	09/2018	66	-3.5	
84	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	439.03	126.43	03/2017 -	11/2018	20	24.53	
85	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	3,150.00	1,308.04	09/2017 12/2018	12/2018	15	0	
86	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE	06/2009	2,915.00 -	2,915.00	1,269.70	12/2012 -	02/2019	74	0	
87	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	10/2015	607.06 714.25	714.25	276.85	10/2017 -	03/2019	17	17.66	
88	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]ONGC,MAHARASHTRA	01/2015	4,619.94 -	3,961.54	3,424.59	12/2017 03/2019	03/2019	15	-14.25	
89	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	390.52 -	390.52	98.70	03/2019 -	04/2019	1	0	
90	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA	11/2014	4,588.29 5,245.96	4,588.29	927.73	08/2018 05/2019	05/2019	9	0	
91	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	571.47	542.29	09/2011 06/2019	06/2019	93	-22.42	
92	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI	08/2014	6,086.08 -	5,479.75	2,148.82	05/2019 10/2019	10/2019	5	-9.96	
93	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 341.70	330.35	3.14	01/2014 11/2019	11/2019	70	62.78	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(October 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
94	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA	08/2015	2,818.88 -	2,818.88	338.56	03/2019 05/2020	05/2020	14	0	
95	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	133.80	07/2018 06/2020	06/2020	23	0	
96	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]BPCL,MAHARASHTRA	02/2016	554.00 -	554.00	25.73	02/2020 -	01/2021	11	0	
	Total		60,194.32 -	63,305.06	38,438.16					
	<u>POWER</u>									
97	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM	07/1998	368.72 1,329.43	1,329.43	1,288.82	07/2006 11/2017	11/2017	136	260.55	
98	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL,MULTI STATE	02/2014	908.08 969.97	969.97	722.47	06/2016 02/2018	11/2017	17	6.82	. Non-availability of down-stream line by HPSEB at Parbati PS shall, however, affect commissioning.
99	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 13,762.80	13,762.80	12,558.71	08/2013 12/2017	12/2017	52	23.65	Balance lines (linked to Gen. Proj.) to be completed matching with Generation).
100	SYSTEM STRENGTHENING XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	245.00	238.62	06/2012 -	12/2017	66	5.45	ROW problem (high compensation)
101	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 1,731.10	1,731.10	1,417.01	11/2012 12/2017	12/2017	61	36.01	
102	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 2,702.65	2,702.65	2,338.48	09/2014 06/2017	12/2017	39	39.3	ROW problem (high compensation).
103	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 346.79	426.29	361.27	08/2014 12/2017	12/2017	40	43.37	Implementation affected due to severe ROW problem in Bengaluru area ROW problem (high compensation)

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(October 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
104	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 2,228.71	2,228.71	1,963.69	08/2014 12/2017	12/2017	40	27.6	
105	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 882.13	882.13	721.43	11/2014 06/2017	12/2017	37	21.9	ROW
106	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	01/2012	15,166.19 -	15,166.19	14,506.00	01/2017 07/2017	12/2017	11	0	
107	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	116.52	04/2016 12/2017	12/2017	20	0	
108	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE	05/2014	829.98 -	829.98	410.67	08/2016 10/2017	12/2017	16	0	Implementation of balance work affected due to disturbance in J&K.
109	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 206.42	206.42	134.03	03/2016 07/2017	12/2017	21	32.69	Implementation of balance affected due to delay in equipment supply(Off-shore) & non-readiness of down stream line by State Govt. at Hamirpur.
110	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 225.28	225.28	133.69	02/2016 08/2017	12/2017	22	14.6	
111	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN,BIHAR	05/2015	436.68 -	602.44	473.75	12/2016 -	12/2017	12	37.96	
112	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH	01/2016	305.04 -	305.04	161.56	03/2017 10/2017	12/2017	9	0	Work slowed-down to match Gen. project (Gen. project ant. by Nov'17).
113	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	135.62	09/2014 09/2017	01/2018	40	0	ROW

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(October 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
114	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A) - [N18000254]PGCIL,MULTI STATE	04/2015	2,525.00 -	2,525.00	1,370.00	11/2017 -	01/2018	2	0	
115	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,882.01	5,073.99	01/2016 -	02/2018	25	61.5	
116	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 5,071.94	5,071.94	4,484.38	10/2012 02/2018	02/2018	64	5.14	
117	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 2,932.88	2,932.88	2,566.17	12/2012 02/2018	02/2018	62	36.79	
118	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 -	539.82	388.72	06/2016 02/2018	02/2018	20	0	ROW problem
119	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 6,179.96	6,179.96	5,990.92	12/2009 03/2018	03/2018	99	147.51	
120	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 738.48	738.48	649.35	09/2010 12/2017	03/2018	90	54.59	ROW
121	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 8,149.00	8,149.00	6,815.00	09/2011 06/2017	03/2018	78	86.25	
122	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99 1,337.76	1,337.76	1,508.72	08/2013 03/2018	03/2018	55	133.06	
123	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 5,135.01	5,135.01	3,464.70	01/2015 03/2018	03/2018	38	16.58	ROW
124	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 703.10	703.10	581.72	06/2015 12/2017	03/2018	33	36.74	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(October 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
125	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	2,011.63	12/2015 12/2017	03/2018	27	0	Implementation affected due to severe ROW problem & huge forest involvement.
126	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 1,891.41	1,891.41	1,166.14	04/2016 09/2017	03/2018	23	38.61	ROW problem
127	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 550.18	550.18	366.29	11/2016 11/2017	03/2018	16	5.34	
128	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE	08/2014	288.49 -	376.09	226.73	02/2017 06/2017	03/2018	13	30.37	Implementation affected due to delay in Transformer supply (failure in testing).
129	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]PGCIL,MULTI STATE	04/2015	1,479.30 -	1,479.30	726.01	04/2017 03/2018	03/2018	11	0	Work has been slowed-down to match with Generation (ant. by Mar'18).
130	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]PGCIL,MULTI STATE	03/2015	955.00 1,161.00	1,364.00	1,083.00	12/2015 -	03/2018	27	42.83	
131	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24 -	1,071.24	465.53	09/2017 -	04/2018	7	0	
132	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	5,151.37	1,622.82	03/2018 -	06/2018	3	0	Completion likely to be delayed due to delay in supply.
133	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE	01/2015	871.62 -	871.62	146.64	10/2017 10/2017	06/2018	8	0	Gen. project delayed.
134	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN	07/2015	307.18 -	307.18	174.58	11/2017 -	06/2018	7	0	. Work slowed-down to extent possible to match the generation.
135	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE	04/2015	3,705.61 -	3,705.61	2,144.69	04/2018 -	07/2018	3	0	Implementation affected due to severe ROW problem & forest clearance (awaited).
136	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,187.32	2,187.32	1,958.79	11/2008 09/2018	09/2018	118	22.93	non-availability of Police protection.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(October 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
137	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 639.46	639.46	485.42	06/2014 03/2018	09/2018	51	31.17	ROW problem (high compensation)
138	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	03/2013	11,638.55 -	11,638.55	8,244.00	09/2017 03/2018	09/2018	12	0	
139	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT - [N18000215]PGCIL,JAMMU AND KASHMIR	01/2014	1,788.41 -	2,333.71	1,204.26	09/2017 -	09/2018	12	30.49	
140	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA	02/2014	12,532.44 -	12,532.44	6,433.00	08/2018 -	11/2018	3	0	
141	PARBATI HEP (4X200 MW) (NHPC) II - [N180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	8,398.75	6,529.67	09/2009 -	12/2018	111	114.28	
142	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	8,128.00	11/2016 12/2017	12/2018	25	0	
143	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	12/2012	11,846.00 -	11,846.00	8,673.00	06/2017 12/2017	12/2018	18	0	
144	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 260.03	260.03	165.86	07/2017 -	12/2018	17	27.92	Project commissioned except Bus Reactor at Yelankha As per MoM of 40th
145	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 294.60	294.60	133.33	02/2014 02/2018	12/2018	58	50.75	Final stage forest clearance for Power Evacuation Arrangement.
146	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 -	13,731.26	10,084.21	01/2018 -	12/2018	11	5.91	
147	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 7,998.00	7,998.00	6,838.73	05/2014 09/2017	02/2019	57	49.41	
148	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	6,957.91	12/2016 -	02/2019	26	0	
149	BARH STPP(3X660MW) NTPC - [N180100242]NTPC,BIHAR	02/2005	8,692.97 15,095.67	15,095.67	13,727.00	01/2011 05/2018	03/2019	98	73.65	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(October 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
150	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	808.63	207.14	01/2018 -	03/2019	14	0	Implementation affected due to forest (Tiger reserve) clearance.
151	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH	09/2014	9,188.98 -	9,188.98	3,231.00	03/2019 -	06/2019	3	0	
152	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	1,394.52	24.47	05/2017 06/2019	06/2019	25	0	Implementation affected due to delayed in land acquisition (land hand over for Dwarka-I S/s in Aug'16 & Rajghat in Dec'16).
153	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	4,754.42	399.63	12/2018 -	12/2019	12	0	Award have been delayed due to poor response & high prices quoted by bidders. Out of 116 Sub stations land for only 45 nos land available.
154	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	5,111.33	363.42	12/2018 -	12/2019	12	0	Award have delayed due to poor response & high prices quoted by bidders.
155	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 -	3,846.30	3,321.00	03/2013 06/2019	03/2020	84	29.14	
156	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 -	14,366.58	5,674.00	02/2019 02/2020	09/2020	19	0	
157	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	2,491.58	1,264.31	06/2013 -	11/2020	89	0	Now the works at various fronts are in progress with intermittent hindrances by villagers. Regular support of Distt. Administration is required.
158	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	3,939.11	2,394.81	02/2016 09/2019	12/2020	58	137.73	Law and order problem Dharna at crusher plan
159	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC, WEST BENGAL	09/2014	1,381.84 -	1,381.84	294.00	09/2019 -	03/2021	18	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(October 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
160	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	881.41	04/2020 12/2017	06/2023	38	0	
	Total		2,23,824.94 -	2,62,161.80	1,78,328.44					
	<u>HEAVY INDUSTRY</u>									
161	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00 -	3,827.30	2,289.00	09/2011 -	12/2017	75	122.78	
	Total		1,718.00 -	3,827.30	2,289.00					
	<u>HEALTH AND FAMILY WELFARE</u>									
162	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC, WEST BENGAL	12/2014	168.90 -	168.90	108.00	05/2017 -	03/2018	10	0	Slow progress on account of labor and material constraints created by the localized unions /goons
163	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC, DELHI	12/2013	204.44 -	204.44	137.00	05/2017 -	06/2018	13	0	
164	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	152.95	34.00	02/2018 -	08/2018	6	0	Progress impacted due to shortage of construction/Building material due to Punjab Govt.
165	AIIMS - OPD(NEW) - [N21000009]HSCC, DELHI	08/2014	293.65 -	293.65	207.00	05/2017 -	09/2018	16	0	
166	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC, MEGHALAYA	10/2016	363.99 -	363.99	14.00	05/2018 08/2019	08/2019	15	0	
	Total		1,183.93 -	1,183.93	500.00					
	<u>RAILWAYS</u>									
167	NANDYAL- YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	966.98	874.72	02/2009 -	12/2017	106	520.89	
168	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	340.00	-	03/2009 03/2009	12/2017	105	154.85	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(October 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
169	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	516.40	710.67	03/2010 -	12/2017	93	58.94	
170	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	1,389.62	1,513.78	03/2014 -	12/2017	45	0	
171	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 495.74	732.89	407.91	06/2013 -	03/2018	57	47.84	
172	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	950.00	679.56	03/2010 -	03/2018	96	38.24	
173	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 -	7,300.00	7,082.91	03/2009 -	03/2018	108	335.48	
174	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 -	5,450.00	4,837.30	04/2008 12/2011	06/2018	122	263.33	
175	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL	03/2013	4,874.58 -	4,874.58	1,881.65	03/2016 -	06/2018	27	0	
176	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 19,565.00	27,946.00	15,803.00	11/2002 -	12/2018	193	1017.84	
177	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	2,913.50	714.40	03/2016 -	12/2018	33	0	
178	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL, TELANGANA	04/2012	632.68 -	816.55	461.84	03/2016 -	12/2018	33	29.06	
179	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	733.00 -	3,040.00	2,389.60	12/2008 -	03/2019	123	314.73	
180	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 -	7,986.04	2,423.55	03/2014 -	03/2019	60	50.68	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(October 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
181	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	321.62	37.15	03/2012 -	03/2019	84	1.06	
182	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	528.57	61.44	03/2018 -	03/2019	12	0	
183	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	941.04	653.42	03/2014 -	06/2019	63	44.07	
184	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 -	1,776.81	967.96	03/1998 -	12/2019	261	359.96	
185	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	1,202.70	482.09	02/2015 -	12/2019	58	556.39	
186	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]RVNL,JHARKHAND	03/1997	261.70 -	388.00	795.83	02/2006 -	12/2019	166	48.26	
187	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	1,161.64	456.30	03/2015 -	12/2019	57	40	
188	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 1,781.98	1,781.98	667.06	03/2004 -	03/2020	192	259.68	
189	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	1,125.89	980.99	12/2011 12/2010	03/2020	99	25.09	
190	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 -	9,658.00	5,464.91	03/2011 -	03/2020	108	1227.45	
191	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	1,825.00	1,410.14	03/2008 06/2008	03/2020	144	145.63	
192	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 -	3,451.00	2,365.89	03/2014 -	03/2020	72	324.3	
193	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34 -	4,600.00	1,749.95	04/2014 -	03/2020	71	642.73	
194	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	4,084.69	383.92	12/2015 -	03/2020	51	204.95	
195	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	385.60	27.69	03/2013 -	03/2020	84	-2.17	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(October 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
196	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00 -	3,000.00	368.41	03/2015 -	03/2020	60	252.94	
197	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	4,259.48	1,464.73	03/2016 -	12/2020	57	7.78	
198	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 -	2,499.71	25.30	03/2021 -	03/2022	12	0	
199	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 -	2,361.74	17.49	03/2021 -	03/2022	12	0	
200	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 -	3,845.60	1.92	02/2020 -	12/2022	34	226.98	
201	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 -	2,030.50	10.34	02/2019 -	12/2022	46	226.23	
202	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	6,093.31	972.82	05/2008 -	03/2023	178	2360.35	
	Total		44,219.60 -	1,22,545.44	59,146.64					
	<u>ROAD TRANSPORT AND HIGHWAYS</u>									
203	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	314.51	06/2008 -	10/2017	112	0	
204	DEOLI KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	593.00	-	07/2013 -	10/2017	51	0	
205	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	351.54	-	05/2013 -	10/2017	53	0	
206	BAREILLY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	577.00	09/2013 -	10/2017	49	0	
207	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	1,573.00	1,850.00	09/2015 -	10/2017	25	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(October 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
208	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]PWD,ANDHRA PRADESH	03/2015	271.45 -	271.45	-	10/2015 -	10/2017	24	0	
209	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	167.64	276.13	11/2008 -	11/2017	108	0	
210	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	245.00	216.62	03/2008 -	11/2017	116	0	
211	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	-	07/2013 -	11/2017	52	0	
212	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	1,112.95	03/2013 -	11/2017	56	0	
213	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	165.67	-	11/2015 -	11/2017	24	0	
214	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	159.12	-	11/2015 -	11/2017	24	0	
215	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	351.34	391.33	01/2016 -	11/2017	22	0	
216	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	495.78	522.62	01/2016 -	11/2017	22	0	
217	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	923.04	481.02	11/2016 -	11/2017	12	0	
218	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	361.00	410.80	02/2009 -	12/2017	106	28.93	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(October 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
219	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	385.13	214.03	04/2009 -	12/2017	104	92.75	
220	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	200.00	250.85	04/2009 -	12/2017	104	0	
221	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	208.00	-	04/2008 -	12/2017	116	0	
222	HARANGAJO TO MAIBANG, NH- 54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	331.23	342.62	07/2009 -	12/2017	101	68.99	
223	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	3,237.87	-	09/2012 -	12/2017	63	114.56	
224	CUDDAPAH-MYDUKUR- KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	2,284.33	05/2013 -	12/2017	55	0	
225	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	-	08/2012 -	12/2017	64	0	
226	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	-	08/2014 -	12/2017	40	0	
227	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	2,051.04	03/2013 -	12/2017	57	0	
228	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,329.10	12/2013 -	12/2017	48	0	
229	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	237.00	05/2013 -	12/2017	55	0	
230	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	406.68	08/2013 -	12/2017	52	0	
231	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	622.89	10/2013 -	12/2017	50	0	
232	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	-	11/2013 -	12/2017	49	0	
233	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	-	06/2014 -	12/2017	42	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(October 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
234	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,400.66	08/2013 -	12/2017	52	0	
235	SIX LANING OF CHANDIKHOL- JAGATPUR-BHUBANESWAR - [N24000205]NHAI, ODISHA	12/2011	1,047.00 -	1,047.00	1,629.83	06/2014 -	12/2017	42	0	
236	6-LANING OF DHANKUNI- KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	1,396.18	2,710.14	09/2014 -	12/2017	39	0	
237	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH	07/2012	291.36 -	291.36	320.46	01/2014 -	12/2017	47	0	
238	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI, UTTARAKHAND	11/2011	478.51 -	478.00	409.17	10/2013 -	12/2017	50	-.11	
239	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI, JHARKHAND	12/2012	1,479.00 -	1,479.00	842.15	06/2015 -	12/2017	30	0	
240	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI, MULTI STATE	10/2012	1,928.22 -	1,928.22	2,488.00	04/2015 -	12/2017	32	0	
241	BARSAT-KRISHNANAGAR - [N24000229]NHAI, WEST BENGAL	08/2012	867.00 -	867.00	278.17	02/2015 -	12/2017	34	0	
242	JALANDHAR - AMRITSAR - [N24000351]NHAI, PUNJAB	01/2014	523.85 -	523.85	250.08	01/2016 -	12/2017	23	0	
243	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI, RAJASTHAN	02/2008	1,673.70 -	1,673.70	3,165.42	10/2011 -	12/2017	74	0	
244	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI, CHHATTISGARH	02/2013	1,232.00 -	1,232.00	-	08/2015 -	12/2017	28	0	
245	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI, MAHARASHTRA	01/2015	972.50 -	972.50	1,460.25	07/2017 -	01/2018	6	0	
246	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, ASSAM	12/2003	160.00 -	160.00	205.46	05/2008 -	02/2018	117	0	
247	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI, HIMACHAL PRADESH	11/2013	1,916.79 -	1,916.79	1,884.41	11/2016 -	02/2018	15	0	
248	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, ASSAM	12/2003	155.04 -	280.13	195.35	11/2008 -	03/2018	112	80.68	
249	BRAHMPUTRA BRIDGE, NH NO- 31 - [N24000063]NHAI, ASSAM	12/2003	217.61 -	309.56	389.87	04/2010 -	03/2018	95	42.25	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(October 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
250	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,882.53	11/2011 -	03/2018	76	106.5	
251	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	-	01/2014 -	03/2018	50	0	
252	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	-	07/2013 -	03/2018	56	0	
253	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	1,555.96	09/2014 -	03/2018	42	0	
254	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,940.09	08/2013 -	03/2018	55	0	
255	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	518.12	07/2014 -	03/2018	44	0	
256	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA	12/2011	942.69 -	942.69	373.84	06/2014 -	03/2018	45	0	
257	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	1,790.50	02/2014 -	03/2018	49	0	
258	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	1,266.60	-	09/2016 -	03/2018	18	0	
259	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	1,655.01	-	08/2016 -	03/2018	19	0	
260	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	1,170.52	2,082.05	06/2012 -	03/2018	69	0	
261	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA) - [N24000527]PWD,ODISHA	12/2011	191.08 -	191.08	-	08/2015 -	03/2018	31	0	
262	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	-	03/2014 -	04/2018	49	0	
263	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	597.00	-	10/2017 -	04/2018	6	0	
264	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	-	02/2013 -	06/2018	64	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(October 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
265	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	563.92	95.89	12/2017 -	06/2018	6	0	
266	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 -	261.09	58.72	05/2017 -	06/2018	13	0	
267	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU	11/2014	563.92 -	563.92	186.50	11/2016 -	06/2018	19	0	
268	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	602.95	266.77	06/2016 -	06/2018	24	0	
269	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	611.65	253.48	06/2016 -	06/2018	24	0	
270	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	641.17	64.90	07/2016 -	07/2018	24	0	
271	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA	06/2016	157.30 157.00	157.00	-	06/2018 -	11/2018	5	-19	
272	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	-	07/2015 -	03/2019	44	0	
273	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	1,012.90	-	03/2016 -	03/2019	36	0	
274	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 -	447.29	51.75	12/2017 -	04/2019	16	0	
275	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	373.07	-	08/2016 -	08/2019	36	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(October 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
276	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	396.52	-	08/2016 -	08/2019	36	0	
277	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 -	429.52	-	08/2016 -	08/2019	36	0	
278	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH	12/2016	138.93 155.00	155.00	-	01/2017 -	01/2020	36	11.57	
	Total		62,070.98 -	65,613.60	45,642.04					
	<u>SHIPPING AND PORTS</u>									
279	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	600.00	139.80	03/2006 -	12/2017	141	300	
280	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 -	669.46	411.12	12/2010 -	12/2018	96	82.72	
	Total		516.39 -	1,269.46	550.92					
	<u>TELECOMMUNICATIONS</u>									
281	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	24,664.00	6,660.00	07/2015 -	06/2019	47	84.97	
	Total		13,334.00 -	24,664.00	6,660.00					
	<u>URBAN DEVELOPMENT</u>									
282	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	332.72	260.88	09/2016 -	11/2017	14	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(October 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
283	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	188.87	166.54	12/2015 12/2017	12/2017	24	0	
284	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 19,058.00	19,058.00	14,784.59	12/2015 -	12/2017	24	30.53	
285	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN - [N28000091]CPWD,RAJASTHAN	08/2014	350.02 479.87	479.87	388.94	03/2015 12/2017	12/2017	33	37.1	
286	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER - [N28000093]CPWD,KERALA	07/2015	154.00 -	154.00	71.90	11/2015 -	12/2017	25	0	
287	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB	02/2014	388.00 -	388.00	289.64	05/2017 02/2018	02/2018	9	0	
288	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	119.37	08/2016 -	03/2018	19	0	
289	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 349.33	349.33	252.50	03/2016 12/2017	03/2018	24	44.75	
290	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 166.97	170.62	146.41	03/2012 -	03/2018	72	-16.77	
291	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	165.23	25.91	10/2012 04/2017	03/2018	65	0	
292	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	884.30	503.45	12/2015 12/2017	03/2018	27	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(October 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
293	CONSTRUCTION OF 1003 NOS 900 NOS TYPE 2 AND 54 NOS TYPE3 AND 33 NOS TYPE 4 AND 16 NOS TYPE 5 FAMILY - [N28000095]CPWD,MADHYA PRADESH	12/2016	164.00 -	164.00	69.24	01/2018 05/2018	05/2018	4	0	
294	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	118.14	11/2014 -	10/2018	47	0	
295	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR	02/2014	216.69 -	216.69	52.00	03/2015 -	11/2018	44	0	
296	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	38.63	03/2016 -	12/2018	33	0	
297	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL	10/2014	162.88 -	162.88	30.74	04/2018 -	06/2019	14	0	
298	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	266.00	-	12/2013 -	10/2019	70	132.8	
299	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	5,181.79	-	07/2017 -	12/2019	29	0	
300	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	8,680.00	1,688.81	03/2018 -	12/2019	21	0	
301	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA	02/2014	26,405.14 -	26,405.14	2,391.46	02/2019 -	03/2020	13	0	land acquisition
302	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 2,230.23	1,592.00	136.13	10/2019 -	03/2020	5	30.58	
	Total		60,252.70 -	65,438.70	21,535.28					
	Grand Total		5,61,421.69	7,07,100.76	4,25,868.82					

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Annexure - VII

(October 2017)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,000.00	09/2010 -	02/2018	71.82	89
	Total		3,492.00 -	6,000.00				
	<u>CIVIL AVIATION</u>							
2	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]	01/2009	309.46 -	553.53	01/2011 -	10/2017	78.87	81
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28	21
	Total		624.07 -	994.86				
	<u>COAL</u>							
4	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	03/2015 -	03/2020	201.44	60
5	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	03/2015 -	03/2020	114.60	60
6	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	03/2012 -	03/2019	80.24	84
7	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI [N06000033]	10/2007	259.40 -	486.57	03/2012 -	03/2018	87.58	72
8	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86	132
9	NEYVELI SOLAR POWER PROJECT 130 MW - [N060000151]	05/2016	687.28 -	830.45	06/2017 -	10/2017	20.83	4
	Total		1,929.87 -	3,064.27				
	<u>FERTILISERS</u>							
10	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY [N08000009]	10/2014	197.79 -	209.44	11/2016 -	04/2019	5.89	29
	Total		197.79 -	209.44				
	<u>HEAVY INDUSTRY</u>							
11	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78	75

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(October 2017)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	Total		1,718.00 -	3,827.30				
	<u>PETROLEUM</u>							
12	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]	06/2010	202.94 -	330.35	01/2014 -	11/2019	62.78	70
13	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	723.40	10/2014 -	03/2018	133.50	41
14	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	439.03	03/2017 -	11/2018	24.53	20
15	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	10/2017 -	03/2019	17.66	17
16	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79 -	1,256.72	05/2013 -	12/2017	45.83	55
17	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	11/2017	37.72	32
18	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	11/2017	70.49	70
19	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	03/2018	29.42	36
20	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]	03/2014	3,076.00 -	4,190.00	09/2017 -	06/2018	36.22	9
21	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	05/2013	4,124.35 -	5,637.00	04/2016 -	12/2017	36.68	20
22	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	06/2014	5,706.47 -	5,813.25	05/2017 -	05/2018	1.87	12
	Total		19,164.96 -	24,662.65				
	<u>POWER</u>							
23	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]	03/2014	155.57 -	206.42	03/2016 -	12/2017	32.69	21
24	DHUKWAN SMALL HYDRO PROJECT - [N18000189]	05/2011	195.42 -	294.60	02/2014 -	12/2018	50.75	58
25	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	02/2014	196.58 -	225.28	02/2016 -	12/2017	14.60	22
26	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03	07/2017 -	12/2018	27.92	17
27	SYSTEM STRENGTHENING XII OF SR - [N18000085]	02/2010	232.34 -	245.00	06/2012 -	12/2017	5.45	66

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(October 2017)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
28	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]	08/2014	288.49 -	376.09	02/2017 -	03/2018	30.37	13
29	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	426.29	08/2014 -	12/2017	43.37	40
30	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	07/1998	368.72 -	1,329.43	07/2006 02/2015	11/2017	260.55	136
31	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]	05/2015	436.68 -	602.44	12/2016 -	12/2017	37.96	12
32	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	738.48	09/2010 -	03/2018	54.59	90
33	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	06/2014 -	09/2018	31.17	51
34	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	03/2013	514.20 -	703.10	06/2015 -	03/2018	36.74	33
35	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	550.18	11/2016 -	03/2018	5.34	16
36	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,337.76	08/2013 -	03/2018	133.06	55
37	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]	11/2011	723.63 -	882.13	11/2014 -	12/2017	21.90	37
38	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	02/2014	908.08 -	969.97	06/2016 -	11/2017	6.82	17
39	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]	03/2015	955.00 -	1,364.00	12/2015 -	03/2018	42.83	27
40	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]	07/2010	1,272.80 -	1,731.10	11/2012 -	12/2017	36.01	61
41	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	04/2016 -	03/2018	38.61	23
42	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	3,939.11	02/2016 -	12/2020	137.73	58
43	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]	12/2011	1,746.65 -	2,228.71	08/2014 -	12/2017	27.60	40
44	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,187.32	11/2008 -	09/2018	22.93	118
45	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI-LEH PROJECT - [N18000215]	01/2014	1,788.41 -	2,333.71	09/2017 -	09/2018	30.49	12
46	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGY PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]	09/2011	1,940.13 -	2,702.65	09/2014 -	12/2017	39.30	39
47	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]	02/2010	2,144.00 -	2,932.88	12/2012 -	02/2018	36.79	62

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(October 2017)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
48	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,179.96	12/2009 06/2016	03/2018	147.51	99
49	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	03/2020	29.14	84
50	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,882.01	01/2016 -	02/2018	61.50	25
51	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	8,398.75	09/2009 -	12/2018	114.28	111
52	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	8,149.00	09/2011 -	03/2018	86.25	78
53	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]	04/2010	4,404.57 -	5,135.01	01/2015 -	03/2018	16.58	38
54	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT [N18000061]	10/2008	4,824.12 -	5,071.94	10/2012 -	02/2018	5.14	64
55	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	7,998.00	05/2014 -	02/2019	49.41	57
56	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	15,095.67	01/2011 -	03/2019	73.65	98
57	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	13,762.80	08/2013 -	12/2017	23.65	52
58	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	13,731.26	01/2018 -	12/2018	5.91	11
	Total		86,011.39 -	1,24,348.25				
	<u>RAILWAYS</u>							
59	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	340.00	03/2009 03/2009	12/2017	154.85	105
60	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	155.74 164.36	966.98	02/2009 -	12/2017	520.89	106
61	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23 -	1,202.70	02/2015 -	12/2019	556.39	58
62	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35	178
63	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1997	261.70 -	388.00	02/2006 -	12/2019	48.26	166
64	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) [N22000123]	04/2008	318.24 -	321.62	03/2012 -	03/2019	1.06	84
65	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	516.40	03/2010 -	12/2017	58.94	93
66	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30 -	1,776.81	03/1998 -	12/2019	359.96	261
67	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	1,781.98	03/2004 -	03/2020	259.68	192

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(October 2017)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
68	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP [N22000028]	04/2006	495.74 -	732.89	06/2013 -	03/2018	47.84	57
69	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	4,600.00	04/2014 -	03/2020	642.73	71
70	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	12/2022	226.23	46
71	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2018	29.06	33
72	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) [N22000113]	04/2008	653.19 -	941.04	03/2014 -	06/2019	44.07	63
73	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	950.00	03/2010 -	03/2018	38.24	96
74	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	9,658.00	03/2011 -	03/2020	1,227.45	108
75	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	3,040.00	12/2008 -	03/2019	314.73	123
76	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 -	1,825.00	03/2008 06/2008	03/2020	145.63	144
77	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	3,451.00	03/2014 -	03/2020	324.30	72
78	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]	04/2008	829.74 -	1,161.64	03/2015 -	12/2019	40.00	57
79	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	850.00 -	3,000.00	03/2015 -	03/2020	252.94	60
80	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]	04/1995	900.05 -	1,125.89	12/2011 12/2010	03/2020	25.09	99
81	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	12/2022	226.98	34
82	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,084.69	12/2015 -	03/2020	204.95	51
83	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	09/1997	1,500.00 -	5,450.00	04/2008 12/2011	06/2018	263.33	122
84	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	7,300.00	03/2009 -	03/2018	335.48	108
85	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	27,946.00	11/2002 -	12/2018	1,017.84	193
86	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	12/2020	7.78	57
87	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68	60
	Total		29,257.73 -	1,07,592.12				

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(October 2017)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
88	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]	12/2016	138.93 155.00	155.00	01/2017 -	01/2020	11.57	36
89	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	03/2018	80.68	112
90	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	12/2017	68.99	101
91	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	12/2017	92.75	104
92	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	04/2010 -	03/2018	42.25	95
93	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	12/2017	28.93	106
94	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	03/2018	106.50	76
95	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]	03/2010	1,509.10 -	3,237.87	09/2012 -	12/2017	114.56	63
	Total		3,804.49 -	7,347.92				
	<u>SHIPPING AND PORTS</u>							
96	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	03/2006 -	12/2017	300.00	141
97	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72	96
	Total		516.39 -	1,269.46				
	<u>STEEL</u>							
98	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]	12/2007	202.61 227.00	227.00	12/2016 -	12/2017	12.04	12
99	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	10/2016 -	03/2018	42.39	17
	Total		545.61 -	715.40				
	<u>TELECOMMUNICATIONS</u>							
100	NETWORK FOR SPECTRUM - [N26000101]	03/2012	13,334.00 -	24,664.00	07/2015 -	06/2019	84.97	47
	Total		13,334.00 -	24,664.00				

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(October 2017)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>URBAN DEVELOPMENT</u>							
101	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101	12/2008	114.26 266.00	266.00	12/2013 -	10/2019	132.80	70
102	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068	02/2011	241.33 -	349.33	03/2016 -	03/2018	44.75	24
103	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN - [N28000091	08/2014	350.02 -	479.87	03/2015 -	12/2017	37.10	33
104	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 -	1,592.00	10/2019 -	03/2020	30.58	5
105	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084	02/2009	14,600.00 -	19,058.00	12/2015 -	12/2017	30.53	24
	Total		16,524.82 -	21,745.20				
	Grand Total		1,77,121.12	3,26,440.87				

Details of Projects Without Date of Commissioning

Annexure - VIII

Costing Rs.150 Crore and above					(October 2017)
					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>COAL</u>				
1	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	12/2012 -	-
2	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND	08/2011	988.35 -	04/2017 -	-
	Total		1,441.98 -		
	<u>MINES</u>				
3	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT RAJASTHAN - [N10000009]NALCO,RAJASTHAN	12/2015	344.50 344.50	11/2016 11/2016	11/2016
4	Implementation of 50.4 MW Wind Power Project at Jath, Sangli, Maharashtra - [N10000008]NALCO,MAHARASHTRA	12/2015	355.13 -	11/2016 12/2016	12/2016
	Total		699.63 -		
	<u>STEEL</u>				
5	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH	04/2014	188.93 -	04/2015 -	-
6	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	12/2015 -	-
7	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	12/2016 -	-
8	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,070.97	02/2014 -	-
9	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 324.87	12/2015 -	-
10	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	01/1999 -	-
11	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL	08/2012	185.37 -	03/2016 -	-
12	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND	02/2014	4,749.00 -	09/2017 -	-
	Total		6,774.27 -		
	<u>PETROLEUM</u>				
13	REPLACEMENT OF KV SECTION OF KSPL - [N16000287]IOCL,GUJARAT	10/2014	279.00 -	08/2018 -	08/2017
14	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	12/2016 06/2017	06/2017
15	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96 -	05/2015 06/2017	06/2017

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above				(October 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
16	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL, RAJASTHAN	11/2011	310.00 -	03/2013 -	-
17	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL, TAMIL NADU	11/2012	678.00 -	02/2017 -	-
	Total		3,251.96 -		
	<u>POWER</u>				
18	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC, UTTARAKHAND	07/2012	1,527.00 -	08/2017 -	08/2017
19	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]DVC, WEST BENGAL	04/2007	4,122.00 8,781.30	02/2011 -	03/2016
20	BOKARO THERMAL POWER STATION-A - [N18000199]DVC, JHARKHAND	08/2006	2,313.00 4,138.41	12/2011 03/2016	02/2017
21	MOUDA STPP STAGE 2 - [N18000132]NTPC, MAHARASHTRA	03/2012	7,921.47 -	09/2016 03/2017	03/2017
22	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]PGCIL, ANDHRA PRADESH	03/2015	550.06 -	03/2018 -	09/2017
23	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC, ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-
24	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO, TRIPURA	07/2009	421.01 1,078.31	07/2013 -	-
25	FGUTPP, UNCHAHAHAR STAGE-IV (1X500 MW) - [N18000174]NTPC, UTTAR PRADESH	07/2013	3,363.12 -	12/2016 -	-
26	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203]NHPC, RAJASTHAN	02/2015	302.49 302.00	02/2016 -	-
	Total		26,805.48 -		
	<u>HEALTH AND FAMILY WELFARE</u>				
27	AIIMS-RAE BARELI-HOUSING - [N21000006]HSCC, UTTAR PRADESH	10/2013	159.50 -	11/2013 06/2017	06/2017
28	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC, DELHI	02/2013	414.11 -	11/2013 -	-
29	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK - [N21000004]HSCC, DELHI	09/2013	444.70 -	12/2015 -	-
30	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005]HSCC, DELHI	11/2013	196.70 -	01/2016 -	-
31	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC, ASSAM	07/2012	175.57 -	12/2014 -	-
	Total		1,390.58 -		
	<u>RAILWAYS</u>				
32	LUMDING-DIBRUGARH (628 KM) INCL. LINK BRANCH LINES OF HAIBARGAON-MAIRABARI (89 KM) - [N22000385]NFR, ASSAM	04/2003	971.22 -	- -	12/2009
33	NEW GUWAHATI-DIGARU-PATCH DOUBLING - [N22000387]NFR, ASSAM	04/2007	180.09 -	- -	05/2011

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above				(October 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
34	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE	12/2006	170.00 -	03/2011 -	10/2011
35	HARMUTI-NAHARLAGUN - [N22000382]NFR,MULTI STATE	04/2006	614.54 -	- -	03/2014
36	DUDHNOI-MENDHIPATHAR - [N22000378]NFR,MULTI STATE	04/1992	315.64 -	- -	11/2014
37	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS - [N22000386]NFR,ASSAM	04/2003	4,300.00 -	- -	08/2015
38	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 -	03/2007 -	04/2016
39	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM	04/1998	227.90 -	12/2012 -	05/2016
40	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]RVNL, WEST BENGAL	04/2010	171.02 -	06/2013 -	12/2016
41	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	02/2009 02/2009	06/2017
42	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	08/2017
43	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 274.56	03/1994 -	-
44	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 -	- -	-
45	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 668.34	06/1999 -	-
46	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR, WEST BENGAL	04/1983	36.80 274.41	- -	-
47	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-
48	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	-
49	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	- -	-
50	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-
51	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-
52	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 -	- -	-
53	KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,062.36	- -	-
54	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-
55	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	06/2004 -	-
56	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	-
57	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 335.77	03/2012 -	-
58	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 -	12/2009 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above				(October 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
59	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	12/2010 -	-
60	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	- 05/2009	-
61	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	744.71 744.71	- -	-
62	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-
63	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-
64	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE	03/1998	280.00 -	- -	-
65	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-
66	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	02/2011 -	-
67	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-
68	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 1,382.78	- -	-
69	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 -	-
70	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-
71	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-
72	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-
73	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-
74	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-
75	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-
76	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- -	-
77	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-
78	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 283.95	03/2012 -	-
79	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' - AGASTIYAMPALLI - [N220000079]SR,TAMIL NADU	09/2007	404.19 -	- -	-
80	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N220000080]SR,TAMIL NADU	09/2006	343.17 -	- -	-
81	TIDIVANAM-NAGARI (NL) - [N220000085]SR,TAMIL NADU	09/2006	456.00 582.83	- 07/2008	-
82	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N220000088]NR,UTTAR PRADESH	04/2006	325.00 -	03/2010 -	-
83	BARDHAMAN-KATWA (GC) - [N220000091]ER, WEST BENGAL	04/2007	1,106.62 -	12/2010 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above				(October 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
84	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-
85	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 -	06/2005 -	-
86	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	282.92 -	- -	-
87	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	03/2013 -	-
88	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL,WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-
89	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	03/2014 -	-
90	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 -	03/2014 -	-
91	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	-
92	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER,WEST BENGAL	04/2009	533.38 -	12/2011 -	-
93	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	611.03 -	12/2011 -	-
94	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER,WEST BENGAL	04/2004	293.74 -	12/2010 -	-
95	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 -	12/2012 -	-
96	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-
97	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-
98	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
99	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
100	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-
101	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-
102	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	- -	-
103	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-
104	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
105	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
106	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	- -	-
107	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above				(October 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
108	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 -	- -	-
109	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	- -	-
110	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-
111	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 -	12/2015 -	-
112	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	- -	-
113	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-
114	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-
115	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-
116	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-
117	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-
118	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-
119	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-
120	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-
121	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-
122	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-
123	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-
124	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-
125	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
126	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-
127	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS (NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-
128	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-
129	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 527.37	- 01/2011	-
130	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-
131	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
132	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above				(October 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
133	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-
134	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
135	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL	04/2010	221.42 -	- -	-
136	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
137	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-
138	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-
139	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 -	- -	-
140	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 -	- -	-
141	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP,WEST BENGAL	04/2009	573.78 -	- -	-
142	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	04/2016 -	-
143	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-
144	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	- -	-
145	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-
146	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-
147	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 1,130.13	- -	-
148	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 -	03/2015 -	-
149	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-
150	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-
151	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-
152	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-
153	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-
154	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRACHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-
155	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above				(October 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
156	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-
157	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-
158	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-
159	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-
160	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-
161	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	03/2017 -	-
162	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-
163	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-
164	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-
165	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-
166	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66 -	03/2017 -	-
167	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	- -	-
168	SANTOSHPUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-
169	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-
170	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	98.74 -	- -	-
171	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	96.16 -	- -	-
172	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-
173	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-
174	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 986.30	- -	-
175	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-
176	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 -	- -	-
177	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-
178	GUDUR-DURGARA JAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above				(October 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
179	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-
180	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-
181	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-
182	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-
183	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-
184	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-
185	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-
186	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-
187	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 692.43	- -	-
188	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-
189	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-
190	RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE	04/2007	970.34 -	- -	-
191	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-
192	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-
193	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
194	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	- -	-
195	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49 -	- -	-
196	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	- -	-
197	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
198	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-
199	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-
200	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-
201	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-
202	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-
203	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above				(October 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
204	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-
205	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-
206	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 1,922.00	- -	-
207	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 367.77	- -	-
208	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-
209	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-
210	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 -	-
211	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-
212	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 279.54	01/1999 -	-
213	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-
214	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	- -	-
215	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	03/2015 -	-
216	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-
217	RAJKHARSWAN - CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	12/2016 -	-
218	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 1,190.92	- -	-
219	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-
220	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-
221	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA	05/2015	400.00 -	- -	-
222	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 1,614.59	- -	-
223	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]NER,UTTAR PRADESH	04/1997	836.26 -	- -	-
224	DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	81,459.00 -	- -	-
225	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA	02/2016	9,968.00 -	- -	-
226	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA	02/2016	2,425.00 -	- -	-
227	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00 -	- -	-
228	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA	02/2015	4,670.00 3,627.00	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above				(October 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
229	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA	02/2016	1,876.00 -	- -	-
230	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	854.00 -	- -	-
231	KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA	04/2013	616.08 -	- -	-
232	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-
233	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	4,000.00 -	- -	-
234	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH	04/2015	3,246.26 -	- -	-
235	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-
236	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-
237	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR,WEST BENGAL	04/2016	556.31 -	- -	-
238	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	900.00 -	- -	-
239	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	- -	-
240	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 -	03/2003 -	-
	Total		2,12,252.77 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
241	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH	06/2017	648.33 -	06/2017 -	06/2017
242	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	07/2017 -	07/2017
243	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	08/2017 -	08/2017
244	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	08/2017 -	08/2017
245	TWO LANE WITH PS OF KARAIKUDI-RAMANATHPURAM - [N24000698]NHAI,TAMIL NADU	08/2017	652.55 -	08/2017 -	08/2017
246	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	09/2017 -	09/2017
247	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH	09/2017	374.40 -	09/2017 -	09/2017
248	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	09/2017 -	09/2017
249	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	09/2017
250	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	09/2017 -	09/2017

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above				(October 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
251	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH	12/2009	165.00 -	09/2010 -	09/2010
252	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH	12/2009	104.00 -	09/2010 -	09/2010
253	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	10/2010 -	10/2010
254	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA	12/2010	1,494.48 -	02/2011 -	02/2011
255	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	02/2011
256	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	10/2013
257	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	10/2013
258	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR	10/2013	278.39 -	08/2014 -	08/2014
259	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA	03/2011	185.82 292.22	- 11/2014	11/2014
260	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA	01/2014	292.98 -	11/2014 -	11/2014
261	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH	11/2011	670.82 -	02/2015 -	02/2015
262	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH	10/2014	213.47 -	03/2015 -	03/2015
263	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH	10/2014	298.34 -	03/2015 -	03/2015
264	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH	11/2014	262.54 -	03/2015 -	03/2015
265	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	381.86 -	04/2015 -	04/2015
266	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH	11/2011	704.26 -	05/2015 -	05/2015
267	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I- - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	08/2015
268	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	08/2015
269	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	11/2015

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above				(October 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
270	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM	01/2016	294.17 -	01/2016 -	01/2016
271	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM	01/2016	252.00 -	01/2016 -	01/2016
272	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH	03/2013	257.80 -	02/2016 -	02/2016
273	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	03/2016
274	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406]MORTH,RAJASTHAN	01/1991	208.87 223.00	05/2016 -	05/2016
275	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH	02/2015	224.83 -	04/2015 -	05/2016
276	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH	02/2014	417.61 -	06/2014 -	06/2016
277	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR	02/2016	369.77 -	06/2016 -	06/2016
278	FUNDED) 2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE - [N24000615]NHIDCL,ARUNACHAL PRADESH	01/2016	334.22 -	06/2016 -	06/2016
279	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOIA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA	08/2014	187.79 -	07/2016 -	07/2016
280	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) - [N24000267]PWD,ANDHRA PRADESH	02/2014	258.99 -	07/2014 -	07/2016
281	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR	01/1991	282.41 -	08/2016 -	08/2016
282	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	871.15 -	09/2015 -	08/2016
283	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	09/2016
284	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH	10/2014	227.74 -	10/2016 -	10/2016
285	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN	01/1991	269.26 -	10/2016 -	10/2016
286	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH	01/2014	397.04 -	10/2016 -	10/2016
287	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR	01/1991	358.22 -	10/2016 -	10/2016
288	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH	10/2013	283.45 -	10/2016 -	10/2016

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above				(October 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
289	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA	12/2013	319.80 -	10/2016 -	10/2016
290	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPROV - [N24000580]MORTH,BIHAR	03/2015	206.80 -	07/2016 -	10/2016
291	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH	04/2016	198.00 -	10/2016 -	10/2016
292	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]NHDP,MAHARASHTRA	06/2014	260.39 -	11/2016 -	11/2016
293	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]NHDP,MAHARASHTRA	12/2013	220.72 -	11/2016 -	11/2016
294	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH	01/2014	195.45 -	11/2014 -	11/2016
295	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH	02/2014	170.21 -	11/2014 -	11/2016
296	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROMKM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH	01/2016	183.65 -	11/2016 -	11/2016
297	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]PWD,TELANGANA	10/2014	244.30 -	12/2016 -	12/2016
298	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH	07/2015	333.21 333.21	12/2015 -	12/2016
299	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	12/2016
300	REHABILATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR	08/2016	1,742.01 -	12/2016 -	12/2016
301	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA	03/2015	153.21 -	01/2017 -	01/2017
302	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA	07/2014	342.05 -	01/2017 -	01/2017
303	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAPUR - [N24000247]PWD,TELANGANA	10/2014	295.47 -	02/2017 -	02/2017
304	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]PWD,ANDHRA PRADESH	02/2015	241.61 -	02/2017 -	02/2017
305	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH	11/2014	297.78 330.00	02/2017 -	02/2017
306	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH	07/2014	251.55 -	02/2015 -	02/2017
307	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	02/2017

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above				(October 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
308	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	03/2017
309	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE - [N24000373]PWD,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	03/2017
310	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH	10/2013	317.76 -	03/2017 -	03/2017
311	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH	10/2013	493.94 -	03/2017 -	03/2017
312	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA	12/2013	319.80 320.00	05/2016 -	03/2017
313	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA	08/2013	171.96 172.00	06/2016 -	03/2017
314	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH,ODISHA	03/2014	162.51 163.00	05/2016 -	03/2017
315	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329]NHIDCL,TRIPURA	05/2014	497.89 -	04/2017 -	04/2017
316	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH	02/2015	224.83 -	05/2015 -	05/2017
317	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH	11/2013	497.05 -	05/2017 -	05/2017
318	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM	11/2010	268.08 -	05/2017 -	05/2017
319	SHAHNOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH	06/2015	532.49 -	05/2017 -	05/2017
320	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH	02/2015	327.32 -	05/2017 -	05/2017
321	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	06/2017
322	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA	01/2014	446.77 -	-	06/2017
323	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA	03/2014	191.50 192.00	05/2016 -	06/2017
324	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	07/2017
325	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	12/2015 -	07/2017
326	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH	02/2015	377.83 -	07/2017 -	07/2017
327	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]NHAI,RAJASTHAN	07/2015	455.60 -	07/2017 -	07/2017

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above				(October 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
328	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	08/2017
329	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	08/2017
330	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	08/2017
331	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDOUT - [N24000300]PWD,ANDHRA PRADESH	03/2015	309.01 -	09/2015 -	08/2017
332	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH	03/2015	511.83 -	08/2017 -	08/2017
333	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA	07/2014	342.05 342.00	01/2017 -	08/2017
334	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	08/2011 -	09/2017
335	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	09/2017
336	MURADABAD-BAREILLY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	06/2013 -	09/2017
337	PATNA-BAKTARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	09/2017
338	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA	01/2014	255.75 348.00	09/2017 -	09/2017
339	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HONNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA	05/2015	709.00 -	09/2017 -	09/2017
340	TWO LANE WITH PAVED SHOULDERS OF CHAS -RAMGARH SECTION OF NH-23 - [N24000343]NHAI,JHARKHAND	09/2015	341.61 -	09/2017 -	09/2017
341	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 -	09/2017
342	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 -	09/2017
343	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	09/2017
344	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	02/2010 -	-
345	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-
346	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	-
347	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-
348	DEVELOPMENT OF ADEQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	-
349	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	-
350	2-LANING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	02/2014 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above				(October 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
351	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-
352	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHTH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	-
353	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI,RAJASTHAN	03/2014	240.10 -	03/2016 -	-
354	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]PWD,TELANGANA	12/2013	177.18 -	03/2016 -	-
355	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPPLY SECTIO - [N24000242]PWD,TELANGANA	12/2013	158.65 -	03/2016 -	-
356	YAN TO NIRMAL SEREHABILITATION AND UPGRADATION OF NH - 222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA	12/2013	244.08 -	03/2016 -	-
357	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD,TELANGANA	01/2014	340.00 -	03/2016 -	-
358	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]PWD,TELANGANA	01/2014	270.00 -	03/2016 -	-
359	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD,TELANGANA	03/2011	218.31 -	12/2015 -	-
360	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA	03/2015	298.33 -	- -	-
361	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]DORTH,GOA	03/2015	184.05 -	- -	-
362	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA	03/2015	280.16 -	- -	-
363	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH	12/2014	201.12 201.00	02/2015 -	-
364	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD,ANDHRA PRADESH	01/2014	361.30 200.69	07/2014 -	-
365	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH	03/2015	175.03 -	- -	-
366	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP - [N24000272]PWD,ANDHRA PRADESH	02/2015	266.00 -	- -	-
367	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH	07/2015	314.43 -	- -	-
368	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA	10/2015	289.60 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above				(October 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
369	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.31	- 03/2013	-
370	CONSTRUCTION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH	12/2010	169.26 -	12/2012 -	-
371	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH	12/2014	394.20 -	- -	-
372	REHABILITATION AND UPGRADE OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH	11/2015	485.44 -	12/2015 -	-
373	REHABILITATION AND UPGRADE OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH	03/2015	422.34 -	- -	-
374	REHABILITATION AND UPGRADE OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB	03/2015	435.90 -	- -	-
375	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB	01/2015	279.68 -	- -	-
376	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB	11/2014	463.65 546.00	- -	-
377	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB	11/2014	573.96 605.00	- -	-
378	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH	10/2015	480.21 -	- -	-
379	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-
380	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-
381	REHABILITATION AND UPGRADE TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-
382	REHABILITATION AND UPGRADE TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-
383	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-
384	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	03/2011 -	-
385	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-
386	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above				(October 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
387	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-
388	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 -	-
389	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 -	08/2013 -	-
390	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 -	08/2013 -	-
391	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 -	02/2013 -	-
392	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-
393	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 268.92	08/2015 -	-
394	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-
395	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH	03/2015	629.74 -	- -	-
396	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-
397	PADI - DAHOD - [N24000353]NHAI,RAJASTHAN	11/2014	279.14 -	05/2017 -	-
398	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]NHAI,RAJASTHAN	10/2014	264.72 -	04/2017 -	-
399	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	-
400	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH	06/2014	301.04 -	01/2016 -	-
401	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB	02/2015	483.38 -	- -	-
402	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB	02/2015	616.36 -	- -	-
403	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB	02/2015	486.74 -	- -	-
404	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	- -	-
405	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-
406	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB	03/2015	312.79 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above				(October 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
407	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOLA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB	07/2014	319.80 -	- -	-
408	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	- -	-
409	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH	01/2011	264.16 -	- -	-
410	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	-
411	4-LANING OF MOGA - TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	- -	-
412	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	- -	-
413	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB	12/2015	578.38 -	- -	-
414	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE	03/2015	789.83 -	- -	-
415	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	-
416	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	-
417	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-
418	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-
419	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	- -	-
420	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	- -	-
421	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA	09/2005	168.00 -	06/2006 -	-
422	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-
423	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	- -	-
424	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	- -	-
425	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- -	-
426	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	- -	-
427	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	- -	-
428	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above					(October 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
429	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98 -	- -	-
430	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-
431	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-
432	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	-
433	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB	06/2015	899.21 -	- -	-
434	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-
435	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-
436	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-
437	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-
438	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR	10/2014	377.64 -	03/2014 -	-
439	MEERUT-BULANDSHAHR - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	- -	-
440	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-
441	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-
442	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	- -	-
443	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	- -	-
444	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	- -	-
445	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	- -	-
446	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	- -	-
447	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above				(October 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
448	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	- -	-
449	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	- -	-
450	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	- -	-
451	FOUR LANING OF TALAJA – MAHUA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT	05/2016	834.64 -	- -	-
452	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	- -	-
453	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	- -	-
454	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	-
455	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	- -	-
456	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR	01/2013	322.01 -	08/2014 -	-
457	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR	11/2013	683.83 -	07/2016 -	-
458	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR	02/2014	665.50 -	07/2016 -	-
459	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR	02/2016	178.85 -	05/2016 -	-
460	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR	02/2016	553.30 -	05/2016 -	-
461	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-
462	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR	08/2015	288.24 -	11/2015 -	-
463	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA	03/2016	1,142.62 -	- -	-
464	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA	03/2016	1,101.58 -	- -	-
465	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	-
466	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above				(October 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
467	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI, GUJARAT	07/2016	829.97 -	- -	-
468	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH - [N24000594]NHAI, JHARKHAND	07/2016	458.03 -	- -	-
469	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI, KARNATAKA	05/2014	720.69 -	- -	-
470	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI, PUNJAB	08/2016	1,169.61 -	- -	-
471	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI, HIMACHAL PRADESH	08/2016	1,583.18 -	- -	-
472	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI, HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-
473	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL, ARUNACHAL PRADESH	04/2016	245.79 -	- -	-
474	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL, ARUNACHAL PRADESH	11/2015	434.06 -	- -	-
475	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI, RAJASTHAN	09/2016	1,239.82 -	- -	-
476	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI, KARNATAKA	09/2016	950.69 -	- -	-
477	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI, RAJASTHAN	09/2016	1,100.19 -	- -	-
478	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI, MULTI STATE	09/2016	1,244.10 -	- -	-
479	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI, MAHARASHTRA	11/2016	1,071.61 -	- -	-
480	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI, MAHARASHTRA	11/2016	1,064.88 -	- -	-
481	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI, MAHARASHTRA	11/2016	290.73 -	- -	-
482	REHABILITAITON AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI, ODISHA	10/2016	1,008.96 -	- -	-
483	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI, HIMACHAL PRADESH	10/2016	447.75 -	- -	-
484	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI, GUJARAT	12/2016	417.19 -	- -	-
485	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI, RAJASTHAN	12/2016	1,031.95 -	- -	-
486	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI, UTTAR PRADESH	12/2016	534.55 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above				(October 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
487	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-
488	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	- -	-
489	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	-
490	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH	01/2017	1,253.10 -	03/2017 -	-
491	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH	03/2017	284.09 -	04/2017 -	-
492	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH	02/2017	195.23 -	04/2017 -	-
493	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH	02/2017	203.36 -	04/2017 -	-
494	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH	01/2017	194.66 -	04/2017 -	-
495	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH	02/2017	168.32 -	04/2017 -	-
496	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 -	04/2017 -	-
497	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH	02/2017	216.71 -	04/2017 -	-
498	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH	02/2017	167.28 -	04/2017 -	-
499	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND	02/2017	507.68 -	04/2017 -	-
500	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH	01/2017	198.22 -	04/2017 -	-
501	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	03/2013 -	06/2017
502	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH	12/2015	291.05 -	- -	-
503	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	-
504	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 -	03/2020 -	-
	Total		1,46,286.80 -		

Details of Projects Without Date of Commissioning

Costing Rs.150 Crore and above				(October 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>SHIPPING AND PORTS</u>				
505	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-
506	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 -	04/2009 -	-
507	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065]KPL,TAMIL NADU	10/2013	198.94 -	06/2017 -	-
508	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED - [N25000067]KPL,TAMIL NADU	12/2014	274.85 -	04/2017 -	-
	Total		3,146.86 -		
	<u>TELECOMMUNICATIONS</u>				
509	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI,MULTI STATE	09/2014	2,111.17 -	09/2014 -	-
510	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI	06/2016	418.26 -	06/2017 -	-
	Total		2,529.43 -		
	<u>URBAN DEVELOPMENT</u>				
511	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	03/2016 -	12/2016
512	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH	06/2014	157.84 -	03/2017 -	-
513	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-
514	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	-
515	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT - [N28000089]CPWD,TAMIL NADU	12/2015	209.00 -	- -	-
516	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	06/2017 -	-
	Total		62,830.92 -		
	Grand Total		4,67,410.68		

Details of Projects Without Original Date of Commissioning

Annexure - IX

Costing Rs.150 Crore and above						(October 2017)			
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>STEEL</u>								
1	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL, GUJARAT	01/2013	175.00 -	175.00	1.83	- -	12/2017	-	0/0
	Total		175.00 -	175.00	1.83				0/0
	<u>RAILWAYS</u>								
2	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER, JHARKHAND	04/2012	258.20 -	365.00	98.37	- -	12/2017	-	0/0
3	ERNAKULAM-KUMBALAM - [N22000204]SR, KERALA	04/2010	189.24 -	189.24	189.35	- -	12/2017	-	0/0
4	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR, KERALA	10/1998	550.00 -	2,815.62	240.68	- -	01/2018	-	0/0
5	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER, BIHAR	04/2003	218.19 -	412.05	356.65	- -	03/2018	-	0/0
6	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER, UTTAR PRADESH	03/2008	195.64 -	474.30	405.98	- -	03/2018	-	0/0
7	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER, UTTAR PRADESH	03/2012	199.75 -	199.75	215.55	- -	03/2018	-	0/0
8	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]RVNL, MULTI STATE	04/2008	822.39 -	1,810.00	1,652.42	- -	03/2018	-	0/1
9	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR, WEST BENGAL	04/2011	209.77 -	630.00	393.80	- -	03/2018	-	0/0
10	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR, MULTI STATE	04/1999	523.17 -	1,871.00	1,071.96	- -	03/2018	-	0/0
11	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR, RAJASTHAN	04/2013	456.00 -	855.16	594.36	- -	05/2018	-	0/0
12	DAUSA-GANGAPUR CITY(NL), NWR - [220100184]NWR, RAJASTHAN	02/1997	410.08 -	780.98	372.98	- -	08/2018	-	0/0
13	CHHAPRA-BALLIA UP - [N22000134]NER, MULTI STATE	03/2013	295.00 -	477.31	97.07	- -	10/2018	-	0/0
14	THIYAT HAMIRA-SANU - [N22000149]NWR, RAJASTHAN	04/2013	236.93 -	276.89	100.50	- -	10/2018	-	0/0
15	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR, RAJASTHAN	04/2012	288.97 335.53	369.08	165.53	- -	10/2018	-	0/0
16	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER, MULTI STATE	04/2010	157.94 -	157.94	47.63	- -	11/2018	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs.150 Crore and above (October 2017)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
17	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	720.00 -	678.54	-	- -	12/2018	-	0/38
18	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 236.41	525.00	544.20	- -	03/2019	-	0/0
19	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	1,319.33	757.23	- 12/2009	03/2019	111(R1)	0/0
20	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	1,185.64	-	- 09/2009	03/2019	114(R1)	0/0
21	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	200.00 -	780.00	427.71	- -	03/2019	-	0/0
22	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	348.55	30.25	- -	03/2019	-	0/0
23	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 -	399.63	-	- -	03/2019	-	0/0
24	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	1,037.15	590.60	- -	03/2019	-	0/0
25	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	272.99	94.92	- -	03/2019	-	0/0
26	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	293.68	128.27	- -	03/2019	-	0/0
27	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 -	1,798.00	-	- -	03/2019	-	0/0
28	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR,WEST BENGAL	04/2012	283.55 -	450.00	194.56	- -	03/2019	-	0/0
29	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	312.12 -	535.00	495.86	- -	03/2019	-	0/0
30	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM	04/2012	246.07 -	398.93	102.71	- -	03/2019	-	0/0
31	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA	04/2010	2,127.00 -	2,127.00	478.01	- -	03/2019	-	0/1
32	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]RVNL,TAMIL NADU	04/2011	190.10 -	350.00	286.57	- -	03/2019	-	0/0
33	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	718.54	275.20	- -	05/2019	-	0/0
34	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	252.00 -	580.00	-	- -	07/2019	-	2/3
35	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	300.00 -	2,135.00	921.06	- -	03/2020	-	0/0
36	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT	04/2012	567.18 -	975.62	2,326.34	- -	03/2020	-	0/0
37	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	4,274.00	-	- -	03/2020	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs.150 Crore and above (October 2017)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Antici Pated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
38	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	165.82 -	450.00	117.50	- -	03/2020	-	0/0
39	VIJAYWADA-GUDUGOLANU-BHIMAVARAM- NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	497.81	- -	03/2020	-	0/0
40	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 -	1,160.83	452.03	- -	03/2020	-	1/1
41	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	238.03	150.50	- -	03/2020	-	0/0
42	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	648.00	.94	- -	03/2020	-	0/0
43	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	860.43	301.48	- -	03/2020	-	0/0
44	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA	03/2015	960.00 578.00	578.00	306.27	- 11/2015	03/2020	52(R3)	0/2
45	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT	04/2012	376.59 -	644.38	28.31	- -	12/2020	-	0/0
46	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,266.89 -	1,548.66	376.11	- -	12/2020	-	0/0
47	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	2,125.18	14.17	- -	03/2021	-	0/0
48	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	470.92 727.13	2,713.09	632.05	- -	03/2021	-	0/0
49	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	4,083.02 -	6,000.00	252.01	- -	03/2021	-	0/0
50	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 792.89	792.89	205.77	- -	03/2021	-	0/0
51	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 -	1,579.27	561.78	- -	03/2021	-	0/0
52	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 -	843.04	41.36	- -	03/2021	-	0/0
53	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	2,063.03	.14	- -	03/2021	-	0/0
54	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32 -	2,232.00	63.61	- -	03/2021	-	0/0
55	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM	04/2015	870.96 -	871.00	21.00	- -	03/2021	-	0/0
56	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 -	1,002.39	-	- -	03/2021	-	0/0
57	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	3,004.90	914.57	- -	06/2021	-	0/0
58	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	378.56 -	1,160.47	1.74	- -	03/2022	-	0/1
59	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	1,640.04	331.91	- -	03/2022	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs.150 Crore and above						(October 2017)			
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
60	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 540.02	540.02	119.78	- -	03/2022	-	0/0
61	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	630.00 1,272.19	1,272.19	53.59	- -	03/2022	-	0/0
62	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	912.00 637.95	637.95	.36	- -	03/2022	-	0/0
63	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	1,928.07	466.10	- -	12/2022	-	0/0
64	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 2,491.43	3,168.29	708.27	- -	03/2023	-	0/0
65	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,326.00 2,449.91	2,449.91	12.78	- -	03/2023	-	0/0
66	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA	01/1991	2,335.67 -	2,335.67	19.87	- -	12/2024	-	0/0
67	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,900.00 1,141.00	1,141.00	448.65	- 03/2020	-	-	0/5
	Total		51,472.84 -	79,999.36	20,756.78				3/52
	ROAD TRANSPORT AND HIGHWAYS								
68	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	2,510.04	-	- -	08/2019	-	0/0
69	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA	03/2015	168.30 -	168.30	13.43	- -	10/2017	-	0/4
70	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	845.24	-	- -	11/2017	-	0/0
71	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB	09/2015	273.06 -	273.06	55.35	- -	11/2017	-	0/0
72	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	946.00	-	- -	12/2017	-	3/3
73	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	479.00	407.76	- -	12/2017	-	0/0
74	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	928.83	-	- -	12/2017	-	0/0
75	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	1,665.00	2,103.52	- -	12/2017	-	0/0
76	TWO LANING WITH PS OF CHHAPRA - GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	854.80	-	- -	12/2017	-	0/0
77	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI,WEST BENGAL	10/2015	361.15 -	361.15	-	- -	01/2018	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs.150 Crore and above						(October 2017)			
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
78	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI,HARYANA	07/2015	1,393.00 -	1,393.00	2,262.08	- -	01/2018	-	0/0
79	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	275.90	-	- -	02/2018	-	0/0
80	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]NHAI,DELHI	09/2015	771.18 -	771.18	559.96	- -	03/2018	-	0/0
81	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHINDEAPAR BRIDGE - [N24000251]NHDP,GOA	03/2015	297.00 -	297.00	38.33	- -	04/2018	-	0/1
82	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	322.09	-	- -	04/2018	-	0/0
83	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	509.13	-	- -	04/2018	-	0/0
84	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 -	726.67	-	- -	04/2018	-	0/0
85	TWO LANING WITH PS OF CHHAPRA - REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR	08/2015	516.13 -	516.13	-	- -	04/2018	-	0/0
86	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	414.00	88.66	- -	05/2018	-	0/0
87	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	531.13	28.10	- -	05/2018	-	0/0
88	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	593.26	-	- -	05/2018	-	0/0
89	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	505.00	76.16	- -	05/2018	-	0/0
90	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA	11/2015	867.66 -	867.66	562.35	- -	05/2018	-	0/0
91	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	596.67	-	- -	05/2018	-	0/0
92	TWO LANING WITH PS OF JOWAI - MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	479.20	-	- -	05/2018	-	0/0
93	UP/HARYANA BORDER - YAMUNA NAGAR - SAHA- BARWALA - PANCHKULA (PKG - 1) - [N24000597]NHAI,HARYANA	05/2015	600.85 -	600.85	264.53	- -	05/2018	-	0/0
94	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	804.97	-	- -	06/2018	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs.150 Crore and above (October 2017)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Antici Pated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
95	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR-HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 -	197.69	-	- -	07/2018	-	0/0
96	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	641.17	-	- -	07/2018	-	0/0
97	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR-HYDERABAD SECTION NS-60 - [N24000561]NHAI,MAHARASHTRA	03/2016	244.00 -	244.00	-	- -	07/2018	-	0/0
98	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	605.84	566.25	- -	07/2018	-	0/0
99	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	1,388.00	-	- -	08/2018	-	0/0
100	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	707.82	129.75	- -	08/2018	-	0/0
101	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	323.72	9.23	- -	08/2018	-	0/0
102	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 -	767.03	66.80	- -	08/2018	-	0/0
103	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	331.46	-	- -	10/2018	-	0/0
104	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	1,423.96	454.64	- -	11/2018	-	0/0
105	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	1,134.97	200.04	- -	11/2018	-	0/0
106	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI,WEST BENGAL	03/2016	229.37 -	229.37	33.96	- -	11/2018	-	0/0
107	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	1,657.20	275.00	- -	01/2019	-	0/0
108	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH	06/2015	1,583.79 -	1,583.79	-	- -	01/2019	-	0/0
109	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN	08/2016	320.30 -	320.30	-	- -	01/2019	-	0/0
110	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH	08/2016	227.49 -	227.49	-	- -	01/2019	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs.150 Crore and above (October 2017)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
111	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	273.20	21.43	- -	02/2019	-	0/0
112	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	649.50	11.42	- -	03/2019	-	0/0
113	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 -	997.15	270.45	- -	03/2019	-	0/0
114	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	1,167.42	-	- -	03/2019	-	0/0
115	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	400.25	-	- -	03/2019	-	0/0
116	4-LANNING OF KODEBAD-DHANTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	446.17	-	- -	03/2019	-	0/0
117	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	2,128.72	249.15	- -	04/2019	-	0/0
118	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	1,041.10	-	- -	04/2019	-	0/0
119	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	399.54	-	- -	04/2019	-	0/0
120	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	676.73	71.78	- -	04/2019	-	0/0
121	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	1,587.49	-	- -	04/2019	-	0/0
122	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	899.00	-	- -	04/2019	-	0/0
123	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	2,016.00	-	- -	04/2019	-	0/0
124	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20 -	1,664.20	-	- -	04/2019	-	0/0
125	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	2,288.18	-	- -	05/2019	-	0/0
126	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	1,885.74	-	- -	05/2019	-	0/0
127	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]NHAI,UTTAR PRADESH	01/2016	701.12 -	701.12	-	- -	05/2019	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs.150 Crore and above						(October 2017)			
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
128	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	248.97	-	- -	05/2019	-	0/0
129	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA	09/2016	1,004.67 -	1,004.67	-	- -	05/2019	-	0/0
130	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	244.90	10.85	- -	05/2019	-	0/0
131	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 -	1,081.57	-	- -	06/2019	-	0/0
132	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	546.00	-	- -	07/2019	-	0/0
133	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	591.66	-	- -	07/2019	-	0/0
134	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 -	1,388.34	-	- -	09/2019	-	0/0
	Total		55,347.20 -	55,346.69	8,830.98				3/8
	URBAN DEVELOPMENT								
135	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI	06/2015	197.33 -	197.33	4.05	- -	04/2019	-	0/2
	Total		197.33 -	197.33	4.05				0/2
	Grand Total		1,07,192.37	1,35,718.38	29,593.64				6/62

Details of Projects Without Milestones w.r.t. Original Schedule

Annexure - X

Costing Rs. 150 Crore and Above				(October 2017)		
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	01/2011 09/2017	10/2017	0/0
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	09/2018 -	06/2020	0/0
	Total		624.07 -			0/0
	<u>COAL</u>					
3	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]NLC,TAMIL NADU	05/2016	687.28 830.45	06/2017 -	10/2017	0/0
4	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN	03/2015	522.45 -	09/2019 -	09/2019	0/0
5	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN	03/2015	513.63 -	12/2019 -	12/2019	0/0
6	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH	07/2016	17,237.00 -	11/2021 -	11/2021	0/0
7	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL,MADHYA PRADESH	07/2016	409.87 -	03/2022 -	03/2022	0/0
8	VIJAY WEST OPENCAST PROJECT - [N06000158]SECL,CHHATISGARH	05/2017	976.95 -	03/2026 -	03/2026	0/0
	Total		20,347.18 -			0/0
	<u>FERTILISERS</u>					
9	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79 209.44	11/2016 04/2019	04/2019	0/0
	Total		197.79 -			0/0
	<u>STEEL</u>					
10	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	12/2016 -	12/2017	0/0
11	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL,GUJARAT	01/2013	175.00 -	- -	12/2017	0/0
12	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	10/2016 -	03/2018	0/0
13	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 253.92	06/2016 -	03/2018	0/0
14	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND	12/2007	200.00 -	03/2018 -	03/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above

(October 2017)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
15	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND	04/2013	170.00 -	04/2018 -	04/2018	0/0
16	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120]RINL,ANDHRA PRADESH	07/2015	465.85 -	07/2018 -	07/2018	0/0
17	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	03/2017 -	08/2018	0/0
18	CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH	08/2015	320.66 -	08/2018 -	08/2018	0/0
19	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH	04/2014	1,682.85 -	09/2018 -	09/2018	0/0
20	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH	12/2011	2,858.00 -	12/2017 -	10/2018	0/0
21	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCP - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	09/2017 -	12/2018	0/0
22	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	12/2016 -	12/2018	0/0
23	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	03/2015 -	03/2021	0/0
24	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	12/2015 -	-	0/0
25	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	12/2016 -	-	0/0
26	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,070.97	02/2014 -	-	0/0
27	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 324.87	12/2015 -	-	0/0
28	CONSTRUCTION OF 123 BLOCKS IN TELEGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	01/1999 -	-	0/0
29	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL	08/2012	185.37 -	03/2016 -	-	0/0
30	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND	02/2014	4,749.00 -	09/2017 -	-	0/0
	Total		15,340.85 -			0/0
	PETROLEUM					
31	REPLACEMENT OF KV SECTION OF KSPL - [N16000287]IOCL,GUJARAT	10/2014	279.00 -	08/2018 -	08/2017	0/0
32	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPL,KARNATAKA	01/2006	993.00 -	01/2012 -	11/2017	0/0
33	SONAMURA GGS AND PIPELINE PROJECT (PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A - [N16000246]ONGC,TRIPURA	05/2016	215.38 -	06/2017 01/2018	01/2018	0/0
34	FUEL QUALITY UPGRADATION (DHDT/DHDS) PROJECT AT GUJARAT REFINERY - [N16000245]IOCL,GUJARAT	02/2016	931.00 -	07/2017 -	02/2018	0/0
35	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM	03/2009	228.64 -	12/2016 -	03/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(October 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
36	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]ONGC,MADHYA PRADESH	03/2009	181.02 -	01/2017 03/2018	03/2018	0/0
37	NEW 250 TMTA LPG PLANT AT PANAGARH - [N16000222]HPCL,WEST BENGAL	08/2014	190.45 -	09/2017 03/2018	03/2018	0/0
38	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA	12/2015	3,190.69 -	04/2018 04/2018	04/2018	0/0
39	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC,MAHARASHTRA	02/2015	2,899.93 -	05/2017 05/2018	05/2018	0/0
40	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT KOCHI REFINERY - [N16000264]BPCL,KERALA	05/2015	337.06 -	08/2018 -	08/2018	0/0
41	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]ONGC,GUJARAT	11/2014	195.63 -	09/2018 09/2018	09/2018	0/0
42	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]ONGC,ANDHRA PRADESH	04/2017	420.76 -	09/2018 09/2018	09/2018	0/0
43	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL,WEST BENGAL	03/2015	694.00 -	10/2018 -	10/2018	0/0
44	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	03/2017 -	11/2018	0/0
45	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]IOCL,BIHAR	07/2015	822.66 -	11/2018 -	11/2018	0/0
46	GAMJI REDEVELOPMENT PROJECT - [N16000202]ONGC,GUJARAT	05/2015	1,671.22 567.22	11/2019 12/2018	12/2018	0/0
47	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY - [N16000262]BPCL,MAHARASHTRA	05/2015	193.40 -	01/2019 -	01/2019	0/0
48	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]IOCL,ODISHA	05/2016	429.00 -	01/2019 -	01/2019	0/0
49	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA	11/2014	6,068.80 6,068.80	04/2019 03/2019	03/2019	0/0
50	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]ONGC,MAHARASHTRA	01/2015	4,619.94 -	12/2017 03/2019	03/2019	0/0
51	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	390.52 -	03/2019 -	04/2019	0/0
52	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY - [N16000290]ONGC,MAHARASHTRA	01/2017	474.15 -	05/2019 -	05/2019	0/0
53	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	09/2011 06/2019	06/2019	0/0
54	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL,MAHARASHTRA	09/2015	4,199.00 -	03/2020 -	07/2019	0/0
55	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI	08/2014	6,086.08 -	05/2019 10/2019	10/2019	0/0
56	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]IOCL,ASSAM	02/2016	2,582.00 -	11/2019 -	11/2019	0/0
57	DEVELOPMENT OF B-147 FIELD - [N16000292]ONGC,MAHARASHTRA	02/2017	546.15 -	11/2019 -	11/2019	0/0
58	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]ONGC,MAHARASHTRA	02/2017	511.30 -	11/2019 -	11/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(October 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
59	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]ONGC,MAHARASHTRA	02/2017	968.61 -	11/2019 -	11/2019	0/0
60	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE	09/2016	571.66 -	12/2019 -	12/2019	0/0
61	MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL,MAHARASHTRA	04/2013	449.58 -	12/2019 -	12/2019	0/0
62	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA	12/2016	161.59 -	12/2019 -	12/2019	0/0
63	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA	02/2015	749.00 -	02/2020 -	02/2020	0/0
64	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA	02/2016	3,313.00 -	02/2020 -	02/2020	0/0
65	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND	02/2017	160.10 -	02/2020 -	02/2020	0/0
66	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA	08/2015	2,818.88 -	03/2019 05/2020	05/2020	0/0
67	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]ONGC,ASSAM	07/2016	249.85 250.00	05/2020 05/2020	05/2020	0/0
68	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	06/2020 -	06/2020	0/0
69	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH	03/2016	34,012.00 -	06/2020 06/2020	06/2020	0/0
70	AUGMENTATION OF CTMPL - [N16000286]IOCL,TAMIL NADU	12/2016	228.00 -	06/2020 -	06/2020	0/0
71	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH	07/2016	20,928.00 -	07/2020 -	07/2020	0/0
72	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]IOCL,GUJARAT	09/2016	208.35 -	07/2020 -	07/2020	0/0
73	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE	05/2016	406.00 -	10/2020 -	10/2020	0/0
74	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 -	12/2020 -	12/2020	0/0
75	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL,WEST BENGAL	04/2016	1,021.00 -	12/2020 -	12/2020	0/0
76	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]BPCL,MAHARASHTRA	02/2016	554.00 -	02/2020 -	01/2021	0/0
77	ADDITIONAL FACILITIES AT MANMAD FOR COVERION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00 -	01/2021 -	01/2021	0/0
78	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 -	01/2021 -	01/2021	0/0
79	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL,MAHARASHTRA	05/2016	261.00 -	01/2021 -	01/2021	0/0
80	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL,ANDHRA PRADESH	01/2015	342.00 -	03/2021 -	03/2021	0/0
81	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL,ANDHRA PRADESH	07/2014	247.00 -	03/2021 -	03/2021	0/0
82	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]ONGC,JHARKHAND	12/2015	658.62 910.23	03/2023 03/2022	03/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2017)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
83	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]GAIL,UTTAR PRADESH	04/2017	287.49 -	04/2022 -	04/2022	0/0
84	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL,ODISHA	07/2017	268.79 -	07/2022 -	07/2022	0/0
85	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]ONGC,GUJARAT	02/2017	1,162.56 1,162.56	03/2026 03/2026	03/2026	0/0
86	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 -	02/2017 -	-	0/0
	Total		1,14,239.07 -			0/0
	<u>POWER</u>					
87	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) - [N18000207]PGCIL,GUJARAT	01/2016	244.19 -	07/2018 -	10/2017	0/0
88	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,552.00	10/2017 12/2016	10/2017	0/0
89	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	04/2016 12/2017	12/2017	0/0
90	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH	01/2016	305.04 -	03/2017 10/2017	12/2017	0/0
91	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]PGCIL,TAMIL NADU	01/2016	162.11 -	05/2018 -	12/2017	0/0
92	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	09/2014 09/2017	01/2018	0/0
93	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A) - [N18000254]PGCIL,MULTI STATE	04/2015	2,525.00 -	11/2017 -	01/2018	0/0
94	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-B - [N18000255]PGCIL,MAHARASHTRA	04/2015	2,225.00 2,225.00	01/2018 -	01/2018	0/0
95	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	03/2018 -	03/2018	0/0
96	50 MW SOLAR POWER PROJECT - [N18000251]NHPC,TAMIL NADU	09/2017	287.48 -	03/2018 -	03/2018	0/0
97	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]PGCIL,MULTI STATE	03/2015	955.00 1,161.00	12/2015 -	03/2018	0/0
98	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24 -	09/2017 -	04/2018	0/0
99	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL	04/2016	454.11 -	04/2018 -	04/2018	0/0
100	NORTH EASTERN REGION STRENGTHENING SCHEME IV - [N18000216]PGCIL,TRIPURA	05/2016	409.19 -	05/2018 -	05/2018	0/0
101	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN	07/2015	307.18 -	11/2017 -	06/2018	0/0
102	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]PGCIL,MADHYA PRADESH	04/2016	287.99 -	06/2018 -	06/2018	0/0
103	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V - [N18000256]PGCIL,MADHYA PRADESH	02/2015	1,750.00 -	06/2018 -	06/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2017)

Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
104	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL, MULTI STATE	07/2015	2,247.37 -	07/2018 -	07/2018	0/0
105	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL, MULTI STATE	01/2016	1,455.47 -	07/2018 -	07/2018	0/0
106	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]PGCIL, ANDHRA PRADESH	01/2016	207.88 -	07/2018 -	07/2018	0/0
107	WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]PGCIL, MULTI STATE	07/2016	150.99 -	07/2018 -	07/2018	0/0
108	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS-KARGIL-KHALSTI-LEH PROJECT - [N18000215]PGCIL, JAMMU AND KASHMIR	01/2014	1,788.41 -	09/2017 -	09/2018	0/0
109	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL, GUJARAT	05/2017	175.64 -	09/2018 -	09/2018	0/0
110	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL, DELHI	05/2015	780.33 -	10/2018 -	10/2018	0/0
111	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]PGCIL, MULTI STATE	05/2016	766.21 -	11/2018 -	11/2018	0/0
112	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]PGCIL, MULTI STATE	05/2016	167.01 -	11/2018 -	11/2018	0/0
113	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I - [N18000220]PGCIL, MULTI STATE	04/2016	810.48 -	12/2018 -	12/2018	0/0
114	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]PGCIL, GUJARAT	07/2016	300.94 -	12/2018 -	12/2018	0/0
115	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJASTHAN - [N18000227]PGCIL, RAJASTHAN	07/2016	1,429.38 -	01/2019 -	01/2019	0/0
116	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL, MULTI STATE	10/2016	408.46 -	01/2019 -	01/2019	0/0
117	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]PGCIL, MULTI STATE	08/2016	431.89 -	02/2019 -	02/2019	0/0
118	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232]PGCIL, MULTI STATE	08/2016	177.52 -	02/2019 -	02/2019	0/0
119	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL, MULTI STATE	02/2017	322.30 -	02/2019 -	02/2019	0/0
120	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL, KARNATAKA	05/2017	445.89 -	02/2019 -	02/2019	0/0
121	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL, MULTI STATE	03/2016	808.63 -	01/2018 -	03/2019	0/0
122	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]PGCIL, MULTI STATE	07/2016	333.17 -	03/2019 -	03/2019	0/0
123	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL, MULTI STATE	09/2016	562.25 -	03/2019 -	03/2019	0/0
124	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODISHA - [N18000243]PGCIL, MULTI STATE	03/2017	162.31 -	03/2019 -	03/2019	0/0
125	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL, ODISHA	04/2016	844.64 -	04/2019 -	04/2019	0/0
126	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION - [N18000237]PGCIL, MULTI STATE	10/2016	167.75 -	04/2019 -	04/2019	0/0
127	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL, MULTI STATE	10/2016	608.24 -	04/2019 -	04/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2017)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
128	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE	12/2015	3,654.00 -	04/2019 -	04/2019	0/0
129	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE	05/2016	3,519.59 -	05/2019 -	05/2019	0/0
130	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]PGCIL,BIHAR	04/2016	790.13 -	06/2019 -	06/2019	0/0
131	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]PGCIL,MULTI STATE	03/2017	251.60 -	06/2019 -	06/2019	0/0
132	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	06/2019 -	06/2019	0/0
133	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE	03/2017	337.75 -	06/2019 -	06/2019	0/0
134	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 -	07/2019 -	07/2019	0/0
135	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]PGCIL,MULTI STATE	02/2017	204.12 -	09/2019 -	09/2019	0/0
136	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE	05/2016	14,733.37 -	11/2019 -	11/2019	0/0
137	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE	03/2017	283.72 -	11/2019 -	11/2019	0/0
138	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE	03/2017	379.95 -	12/2019 -	12/2019	0/0
139	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	12/2018 -	12/2019	0/0
140	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	12/2018 -	12/2019	0/0
141	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]PGCIL,MULTI STATE	02/2017	195.05 -	02/2020 -	02/2020	0/0
142	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE	08/2017	1,931.39 -	02/2020 -	02/2020	0/0
143	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL,MULTI STATE	02/2017	5,070.13 -	04/2020 -	04/2020	0/0
144	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE	03/2017	3,500.00 3,500.00	07/2020 -	07/2020	0/0
145	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	04/2020 12/2017	06/2023	0/0
146	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-	0/0
	Total		91,081.01 -			0/0
	HEAVY INDUSTRY					
147	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00 -	09/2011 -	12/2017	0/0
	Total		1,718.00 -			0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2017)

			Date of Commissioning (Month/Year)			
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	HEALTH AND FAMILY WELFARE					
148	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC, WEST BENGAL	08/2016	244.00 -	09/2018 -	09/2018	0/0
149	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASHTRA - [N21000016]HSCC, MAHARASHTRA	08/2017	274.19 -	03/2019 -	03/2019	0/0
150	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC, ANDHRA PRADESH	08/2017	272.19 -	03/2019 -	03/2019	0/0
151	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC, WEST BENGAL	08/2017	355.15 -	03/2019 -	03/2019	0/0
152	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC, MEGHALAYA	10/2016	363.99 -	05/2018 08/2019	08/2019	0/0
153	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC, DELHI	02/2013	414.11 -	11/2013 -	-	0/0
154	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS - SUPER SPECIALITY BLOCK - [N21000004]HSCC, DELHI	09/2013	444.70 -	12/2015 -	-	0/0
155	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005]HSCC, DELHI	11/2013	196.70 -	01/2016 -	-	0/0
156	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC, ASSAM	07/2012	175.57 -	12/2014 -	-	0/0
	Total		2,740.60 -			0/0
	RAILWAYS					
157	LUMDING-DIBRUGARH (628 KM) INCL. LINK BRANCH LINES OF HAIBARGAON-MAIRABARI (89 KM) - [N22000385]NFR, ASSAM	04/2003	971.22 -	- -	12/2009	0/0
158	NEW GUWAHATI-DIGARU-PATCH DOUBLING - [N22000387]NFR, ASSAM	04/2007	180.09 -	- -	05/2011	0/0
159	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR, MULTI STATE	12/2006	170.00 -	03/2011 -	10/2011	0/0
160	HARMUTI-NAHARLAGUN - [N22000382]NFR, MULTI STATE	04/2006	614.54 -	- -	03/2014	0/0
161	DUDHNOI-MENDHIPATHAR - [N22000378]NFR, MULTI STATE	04/1992	315.64 -	- -	11/2014	0/0
162	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS - [N22000386]NFR, ASSAM	04/2003	4,300.00 -	- -	08/2015	0/0
163	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR, TRIPURA	04/1999	895.00 -	03/2007 -	04/2016	0/0
164	KATAKHAL TO BHAIRABI - [N22000126]NFR, ASSAM	04/1998	227.90 -	12/2012 -	05/2016	0/0
165	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]RVNL, WEST BENGAL	04/2010	171.02 -	06/2013 -	12/2016	0/0
166	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER, MULTI STATE	03/2007	243.78 -	- -	08/2017	0/0
167	NANDYAL-YERRAGUNTALA(NL), SCR - [220100192]SCR, ANDHRA PRADESH	03/1996	155.74 164.36	02/2009 -	12/2017	0/0
168	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR, GUJARAT	04/2008	1,389.62 -	03/2014 -	12/2017	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2017)

Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
169	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 -	- -	12/2017	0/0
170	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	12/2017	0/0
171	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 -	- -	01/2018	0/0
172	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	- -	03/2018	0/0
173	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	03/2010 -	03/2018	0/0
174	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 -	03/2009 -	03/2018	0/0
175	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	03/2018	0/0
176	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	- -	03/2018	0/0
177	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR,WEST BENGAL	04/2011	209.77 -	- -	03/2018	0/0
178	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE	04/1999	523.17 -	- -	03/2018	0/0
179	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	03/2018 -	03/2018	0/0
180	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH	01/2013	387.70 -	03/2018 -	03/2018	0/0
181	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH	05/2014	207.00 -	03/2018 -	03/2018	0/0
182	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	- -	05/2018	0/0
183	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 -	04/2008 12/2011	06/2018	0/0
184	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	06/2018	0/0
185	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	- -	08/2018	0/0
186	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	- -	10/2018	0/0
187	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	10/2018	0/0
188	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 335.53	- -	10/2018	0/0
189	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	11/2018	0/0
190	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 19,565.00	11/2002 -	12/2018	0/0
191	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	03/2016 -	12/2018	0/0
192	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	03/2016 -	12/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2017)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
193	MUNEERABAD-MAHABOBNAGAR(NL), SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 236.41	- -	03/2019	0/0
194	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	733.00 -	12/2008 -	03/2019	0/0
195	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	- 12/2009	03/2019	0/0
196	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, ODISHA	04/1996	301.64 -	- 09/2009	03/2019	0/0
197	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	200.00 -	- -	03/2019	0/0
198	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 -	03/2014 -	03/2019	0/0
199	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR, GUJARAT	04/2008	318.24 -	03/2012 -	03/2019	0/0
200	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR, RAJASTHAN	04/2012	246.08 -	- -	03/2019	0/0
201	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR, GUJARAT	04/1994	320.66 -	- -	03/2019	0/0
202	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR, GUJARAT	04/2011	446.00 -	- -	03/2019	0/0
203	AJMER-BANGURGRAM - [N22000155]NWR, RAJASTHAN	04/2011	213.39 -	- -	03/2019	0/0
204	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR, RAJASTHAN	04/2013	242.09 -	- -	03/2019	0/0
205	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR, MULTI STATE	04/2013	1,798.00 -	- -	03/2019	0/0
206	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR, WEST BENGAL	04/2012	283.55 -	- -	03/2019	0/0
207	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR, ASSAM	04/2011	312.12 -	- -	03/2019	0/0
208	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR, ASSAM	04/2012	246.07 -	- -	03/2019	0/0
209	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]RVNL, TAMIL NADU	04/2011	190.10 -	- -	03/2019	0/0
210	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL, UTTAR PRADESH	04/2011	927.01 -	03/2019 -	03/2019	0/0
211	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL, ODISHA	03/2009	942.95 -	03/2019 -	03/2019	0/0
212	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR, UTTAR PRADESH	08/2015	528.57 -	03/2018 -	03/2019	0/0
213	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI, MAHARASHTRA	10/2013	305.00 -	03/2019 -	03/2019	0/0
214	MULTI MODAL LOGISTICS PARK AT SWARUPGANJ - [N22000423]CCOI, RAJASTHAN	04/2012	471.82 -	03/2019 -	03/2019	0/0
215	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI, HARYANA	12/2015	346.32 -	03/2019 -	03/2019	0/0
216	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI, MADHYA PRADESH	12/2015	174.00 -	03/2019 -	03/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(October 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
217	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI, GUJARAT	10/2013	343.00 -	03/2019 -	03/2019	0/0
218	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI, ANDHRA PRADESH	08/2016	234.50 -	03/2019 -	03/2019	0/0
219	HATHUA-BHATNI (N L) (NER) - [220100319]NER, MULTI STATE	04/2005	230.03 -	- -	05/2019	0/0
220	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113]NWR, RAJASTHAN	04/2008	653.19 -	03/2014 -	06/2019	0/0
221	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, MULTI STATE	02/1997	386.30 -	03/1998 -	12/2019	0/0
222	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA	04/1998	183.23 -	02/2015 -	12/2019	0/0
223	HIMMATNAGAR - UDAIPUR GAUGE CONVERSION (NWR) - [N22000112]NWR, RAJASTHAN	04/2008	829.74 -	03/2015 -	12/2019	0/0
224	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP, MAHARASHTRA	03/1996	495.44 1,781.98	03/2004 -	03/2020	0/0
225	MANDARHILL-DUMKA-RAMPURHAT (NL), ER - [220100168]ER, JHARKHAND	04/1995	900.05 -	12/2011 12/2010	03/2020	0/0
226	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR	04/2003	727.56 -	03/2011 -	03/2020	0/0
227	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	03/2020	0/0
228	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR, BIHAR	09/2006	300.00 -	- -	03/2020	0/0
229	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA	04/2008	813.34 -	03/2014 -	03/2020	0/0
230	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	619.34 -	04/2014 -	03/2020	0/0
231	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48 -	12/2015 -	03/2020	0/0
232	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR, GUJARAT	04/2008	394.14 -	03/2013 -	03/2020	0/0
233	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND	04/2006	850.00 -	03/2015 -	03/2020	0/0
234	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL, GUJARAT	04/2012	567.18 -	- -	03/2020	0/0
235	DIMAPUR-TIZIT NL - [N22000196]NFR, NAGALAND	04/2013	4,274.00 -	- -	03/2020	0/0
236	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR, MULTI STATE	04/2011	165.82 -	- -	03/2020	0/0
237	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL, ANDHRA PRADESH	03/2012	1,503.71 -	- -	03/2020	0/0
238	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR, ODISHA	03/2012	155.81 -	- -	03/2020	0/0
239	PHULERA - DIGANA DOUBLING - [N22000326]NWR, MULTI STATE	05/2015	600.00 -	- -	03/2020	0/0
240	YELAHANKA-PENUKONDA - [N22000328]SWR, MULTI STATE	05/2015	860.43 -	- -	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(October 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
241	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 -	03/2021 -	03/2020	0/0
242	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 -	03/2020 -	03/2020	0/0
243	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	1,514.45 -	03/2020 -	03/2020	0/0
244	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	960.18 -	03/2020 -	03/2020	0/0
245	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	758.09 -	03/2020 -	03/2020	0/0
246	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	03/2020 -	03/2020	0/0
247	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]ECOR,ODISHA	04/2016	5,200.00 -	03/2020 -	03/2020	0/0
248	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	03/2016 -	12/2020	0/0
249	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT	04/2012	376.59 -	- -	12/2020	0/0
250	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,266.89 -	- -	12/2020	0/0
251	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	12/2020 -	12/2020	0/0
252	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH	04/2011	1,485.65 -	12/2020 -	12/2020	0/0
253	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	- -	03/2021	0/0
254	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	470.92 727.13	- -	03/2021	0/0
255	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	4,083.02 -	- -	03/2021	0/0
256	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 792.89	- -	03/2021	0/0
257	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 -	- -	03/2021	0/0
258	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 -	- -	03/2021	0/0
259	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	- -	03/2021	0/0
260	JAGDALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 -	03/2021 -	03/2021	0/0
261	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	03/2021 -	03/2021	0/0
262	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32 -	- -	03/2021	0/0
263	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM	04/2015	870.96 -	- -	03/2021	0/0
264	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 -	- -	03/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2017)

			Date of Commissioning (Month/Year)			
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
265	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	03/2021 -	03/2021	0/0
266	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	- -	06/2021	0/0
267	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]SER, WEST BENGAL	01/1991	763.18 -	12/2021 -	12/2021	0/0
268	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]SER,ODISHA	04/1995	524.43 -	12/2021 -	12/2021	0/0
269	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA	09/2016	1,273.00 1,908.00	12/2021 -	12/2021	0/0
270	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	- -	03/2022	0/0
271	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 540.02	- -	03/2022	0/0
272	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH	03/2015	1,750.00 -	03/2022 -	03/2022	0/0
273	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	630.00 1,272.19	- -	03/2022	0/0
274	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	912.00 637.95	- -	03/2022	0/0
275	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 -	03/2021 -	03/2022	0/0
276	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 -	03/2021 -	03/2022	0/0
277	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	- -	12/2022	0/0
278	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 -	02/2020 -	12/2022	0/0
279	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 -	02/2019 -	12/2022	0/0
280	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 2,491.43	- -	03/2023	0/0
281	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,326.00 2,449.91	- -	03/2023	0/0
282	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	750.55 -	12/2024 -	12/2024	0/0
283	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA	04/2015	728.10 -	12/2024 -	12/2024	0/0
284	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA	01/1991	2,335.67 -	- -	12/2024	0/0
285	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.90 -	12/2025 -	12/2025	0/0
286	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA	04/2015	723.78 -	12/2025 -	12/2025	0/0
287	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	4,295.30 -	12/2026 -	12/2026	0/0
288	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 274.56	03/1994 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(October 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
289	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 -	- -	-	0/0
290	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 668.34	06/1999 -	-	0/0
291	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	36.80 274.41	- -	-	0/0
292	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-	0/0
293	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	-	0/0
294	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	- -	-	0/0
295	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-	0/0
296	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-	0/0
297	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 -	- -	-	0/0
298	KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,062.36	- -	-	0/0
299	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-	0/0
300	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	06/2004 -	-	0/0
301	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	-	0/0
302	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 335.77	03/2012 -	-	0/0
303	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 -	12/2009 -	-	0/0
304	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	12/2010 -	-	0/0
305	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-	0/0
306	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-	0/0
307	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-	0/0
308	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	02/2011 -	-	0/0
309	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-	0/0
310	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 1,382.78	- -	-	0/0
311	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 -	-	0/0
312	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(October 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
313	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-	0/0
314	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-	0/0
315	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-	0/0
316	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-	0/0
317	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-	0/0
318	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- -	-	0/0
319	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-	0/0
320	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 283.95	03/2012 -	-	0/0
321	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	- -	-	0/0
322	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	- -	-	0/0
323	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 582.83	- 07/2008	-	0/0
324	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 -	03/2010 -	-	0/0
325	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-	0/0
326	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 -	06/2005 -	-	0/0
327	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	282.92 -	- -	-	0/0
328	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII-MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	03/2013 -	-	0/0
329	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-	0/0
330	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	-	0/0
331	SURATPURA - HANUMANGARH - SRIGANGANAGAR GAUGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 -	03/2014 -	-	0/0
332	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	-	0/0
333	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	533.38 -	12/2011 -	-	0/0
334	GHUTIASARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL	04/2009	611.03 -	12/2011 -	-	0/0
335	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	293.74 -	12/2010 -	-	0/0
336	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL	04/1999	207.52 -	12/2012 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(October 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
337	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-	0/0
338	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-	0/0
339	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0
340	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
341	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-	0/0
342	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-	0/0
343	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	- -	-	0/0
344	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0
345	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- -	-	0/0
346	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 -	- -	-	0/0
347	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	- -	-	0/0
348	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-	0/0
349	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 -	12/2015 -	-	0/0
350	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	- -	-	0/0
351	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-	0/0
352	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-	0/0
353	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-	0/0
354	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-	0/0
355	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-	0/0
356	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-	0/0
357	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-	0/0
358	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-	0/0
359	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-	0/0
360	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(October 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
361	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-	0/0
362	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-	0/0
363	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-	0/0
364	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-	0/0
365	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-	0/0
366	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-	0/0
367	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 527.37	- 01/2011	-	0/0
368	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-	0/0
369	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-	0/0
370	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-	0/0
371	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-	0/0
372	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-	0/0
373	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL	04/2010	221.42 -	- -	-	0/0
374	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-	0/0
375	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-	0/0
376	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-	0/0
377	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 -	- -	-	0/0
378	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 -	- -	-	0/0
379	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSHUPUR - [N22000212]MRTP,WEST BENGAL	04/2009	573.78 -	- -	-	0/0
380	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	04/2016 -	-	0/0
381	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-	0/0
382	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	- -	-	0/0
383	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2017)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
384	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-	0/0
385	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 1,130.13	- -	-	0/0
386	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 -	03/2015 -	-	0/0
387	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-	0/0
388	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-	0/0
389	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-	0/0
390	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-	0/0
391	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-	0/0
392	SONDALIA-CHAMPAPUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-	0/0
393	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-	0/0
394	BARIAPIUR-MANANPUR VIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-	0/0
395	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-	0/0
396	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-	0/0
397	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-	0/0
398	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-	0/0
399	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	03/2017 -	-	0/0
400	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-	0/0
401	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-	0/0
402	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-	0/0
403	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-	0/0
404	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66 -	03/2017 -	-	0/0
405	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	- -	-	0/0
406	SANTOSHAPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-	0/0
407	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(October 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
408	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	98.74 -	- -	-	0/0
409	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	96.16 -	- -	-	0/0
410	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-	0/0
411	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 -	- -	-	0/0
412	GUDUR-DURGARAJPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-	0/0
413	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-	0/0
414	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-	0/0
415	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-	0/0
416	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-	0/0
417	DELHI-SOHNANUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-	0/0
418	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-	0/0
419	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-	0/0
420	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-	0/0
421	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 692.43	- -	-	0/0
422	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-	0/0
423	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-	0/0
424	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-	0/0
425	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-	0/0
426	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-	0/0
427	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-	0/0
428	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-	0/0
429	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-	0/0
430	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-	0/0
431	UNCHAHAAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(October 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
432	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-	0/0
433	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-	0/0
434	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-	0/0
435	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 1,922.00	- -	-	0/0
436	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 367.77	- -	-	0/0
437	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-	0/0
438	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-	0/0
439	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 -	-	0/0
440	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-	0/0
441	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 279.54	01/1999 -	-	0/0
442	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-	0/0
443	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	- -	-	0/0
444	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	03/2015 -	-	0/0
445	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-	0/0
446	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	12/2016 -	-	0/0
447	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 1,190.92	- -	-	0/0
448	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-	0/0
449	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-	0/0
450	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA	05/2015	400.00 -	- -	-	0/0
451	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 1,614.59	- -	-	0/0
452	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]NER,UTTAR PRADESH	04/1997	836.26 -	- -	-	0/0
453	DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	81,459.00 -	- -	-	0/0
454	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA	02/2016	9,968.00 -	- -	-	0/0
455	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA	02/2016	2,425.00 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(October 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
456	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00 -	- -	-	0/0
457	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA	02/2015	4,670.00 3,627.00	- -	-	0/0
458	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA	02/2016	1,876.00 -	- -	-	0/0
459	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	854.00 -	- -	-	0/0
460	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-	0/0
461	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	4,000.00 -	- -	-	0/0
462	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH	04/2015	3,246.26 -	- -	-	0/0
463	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-	0/0
464	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-	0/0
465	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR,WEST BENGAL	04/2016	556.31 -	- -	-	0/0
466	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	900.00 -	- -	-	0/0
467	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	- -	-	0/0
468	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 -	03/2003 -	-	0/0
	Total		3,20,662.25 -			0/0
	ROAD TRANSPORT AND HIGHWAYS					
469	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	03/2020 -	03/2020	0/0
470	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH	06/2017	648.33 -	06/2017 -	06/2017	0/0
471	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	07/2017 -	07/2017	0/0
472	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	08/2017 -	08/2017	0/0
473	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	08/2017 -	08/2017	0/0
474	TWO LANE WITH PS OF KARAUKUDI-RAMANATHPURAM - [N24000698]NHAI,TAMIL NADU	08/2017	652.55 -	08/2017 -	08/2017	0/0
475	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	- -	08/2019	0/0
476	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	09/2017 -	09/2017	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(October 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
477	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH	09/2017	374.40 -	09/2017 -	09/2017	0/0
478	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	09/2017 -	09/2017	0/0
479	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	09/2017	0/0
480	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	09/2017 -	09/2017	0/0
481	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	10/2017	0/0
482	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	10/2017 -	10/2017	0/0
483	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	10/2017 -	10/2017	0/0
484	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH	12/2009	165.00 -	09/2010 -	09/2010	0/0
485	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH	12/2009	104.00 -	09/2010 -	09/2010	0/0
486	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	10/2010 -	10/2010	0/0
487	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA	12/2010	1,494.48 -	02/2011 -	02/2011	0/0
488	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	02/2011	0/0
489	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	10/2013	0/0
490	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	10/2013	0/0
491	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR	10/2013	278.39 -	08/2014 -	08/2014	0/0
492	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA	03/2011	185.82 292.22	- 11/2014	11/2014	0/0
493	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA	01/2014	292.98 -	11/2014 -	11/2014	0/0
494	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH	11/2011	670.82 -	02/2015 -	02/2015	0/0
495	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH	10/2014	213.47 -	03/2015 -	03/2015	0/0
496	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH	10/2014	298.34 -	03/2015 -	03/2015	0/0
497	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH	11/2014	262.54 -	03/2015 -	03/2015	0/0
498	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	381.86 -	04/2015 -	04/2015	0/0
499	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH	11/2011	704.26 -	05/2015 -	05/2015	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(October 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
500	CONSTRUCTION OF PAVED SHOULDERS INCLUDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	08/2015	0/0
501	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	08/2015	0/0
502	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	11/2015	0/0
503	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH	03/2013	257.80 -	02/2016 -	02/2016	0/0
504	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	03/2016	0/0
505	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406]MORTH,RAJASTHAN	01/1991	208.87 223.00	05/2016 -	05/2016	0/0
506	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH	02/2015	224.83 -	04/2015 -	05/2016	0/0
507	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR	02/2016	369.77 -	06/2016 -	06/2016	0/0
508	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR	01/1991	282.41 -	08/2016 -	08/2016	0/0
509	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	871.15 -	09/2015 -	08/2016	0/0
510	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	09/2016	0/0
511	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH	10/2014	227.74 -	10/2016 -	10/2016	0/0
512	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN	01/1991	269.26 -	10/2016 -	10/2016	0/0
513	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH	01/2014	397.04 -	10/2016 -	10/2016	0/0
514	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR	01/1991	358.22 -	10/2016 -	10/2016	0/0
515	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH	10/2013	283.45 -	10/2016 -	10/2016	0/0
516	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA	12/2013	319.80 -	10/2016 -	10/2016	0/0
517	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPROV - [N24000580]MORTH,BIHAR	03/2015	206.80 -	07/2016 -	10/2016	0/0
518	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROMKM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH	01/2016	183.65 -	11/2016 -	11/2016	0/0
519	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH.0.0) - [N24000302]PWD,ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	12/2016	0/0
520	REHABILATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR	08/2016	1,742.01 -	12/2016 -	12/2016	0/0
521	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA	03/2015	153.21 -	01/2017 -	01/2017	0/0
522	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA	07/2014	342.05 -	01/2017 -	01/2017	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (October 2017)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
523	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH	11/2014	297.78 330.00	02/2017 -	02/2017	0/0
524	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	02/2017	0/0
525	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	03/2017	0/0
526	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE - [N24000373]PWD,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	03/2017	0/0
527	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH	10/2013	317.76 -	03/2017 -	03/2017	0/0
528	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH	10/2013	493.94 -	03/2017 -	03/2017	0/0
529	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA	12/2013	319.80 320.00	05/2016 -	03/2017	0/0
530	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA	08/2013	171.96 172.00	06/2016 -	03/2017	0/0
531	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH,ODISHA	03/2014	162.51 163.00	05/2016 -	03/2017	0/0
532	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH	11/2013	497.05 -	05/2017 -	05/2017	0/0
533	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM	11/2010	268.08 -	05/2017 -	05/2017	0/0
534	SHAHNOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH	06/2015	532.49 -	05/2017 -	05/2017	0/0
535	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH	02/2015	327.32 -	05/2017 -	05/2017	0/0
536	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	06/2017	0/0
537	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA	03/2014	191.50 192.00	05/2016 -	06/2017	0/0
538	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	07/2017	0/0
539	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH	02/2015	377.83 -	07/2017 -	07/2017	0/0
540	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]NHAI,RAJASTHAN	07/2015	455.60 -	07/2017 -	07/2017	0/0
541	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	08/2017	0/0
542	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	08/2017	0/0
543	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	08/2017	0/0
544	UMARIYA TO SHAHNOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH	03/2015	511.83 -	08/2017 -	08/2017	0/0
545	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA	07/2014	342.05 342.00	01/2017 -	08/2017	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(October 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
546	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	09/2017	0/0
547	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	06/2013 -	09/2017	0/0
548	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	09/2017	0/0
549	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA	01/2014	255.75 348.00	09/2017 -	09/2017	0/0
550	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA	05/2015	709.00 -	09/2017 -	09/2017	0/0
551	TWO LANE WITH PAVED SHOULDERS OF CHAS -RAMGARH SECTION OF NH-23 - [N24000343]NHAI,JHARKHAND	09/2015	341.61 -	09/2017 -	09/2017	0/0
552	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 -	09/2017	0/0
553	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 -	09/2017	0/0
554	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	09/2017	0/0
555	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 -	10/2017	0/0
556	DEOLI KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	07/2013 -	10/2017	0/0
557	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	10/2017	0/0
558	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	10/2017	0/0
559	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	10/2017	0/0
560	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]PWD,ANDHRA PRADESH	03/2015	271.45 -	10/2015 -	10/2017	0/0
561	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAP - [N24000379]MORTH,ODISHA	01/1991	218.63 251.92	10/2017 -	10/2017	0/0
562	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA	02/2015	239.91 240.00	10/2017 -	10/2017	0/0
563	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH,ODISHA	03/2015	226.31 226.00	10/2017 -	10/2017	0/0
564	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM	04/2017	388.00 -	10/2017 -	10/2017	0/0
565	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	11/2017	0/0
566	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 -	11/2017	0/0
567	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	11/2017	0/0
568	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	11/2017	0/0
569	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA	01/2014	267.16 352.00	11/2017 -	11/2017	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(October 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
570	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	11/2015 -	11/2017	0/0
571	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	11/2015 -	11/2017	0/0
572	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	11/2017 -	11/2017	0/0
573	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	01/2016 -	11/2017	0/0
574	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	01/2016 -	11/2017	0/0
575	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	11/2017	0/0
576	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- -	11/2017	0/0
577	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB	09/2015	273.06 -	- -	11/2017	0/0
578	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA	12/2011	159.39 -	11/2017 -	11/2017	0/0
579	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	12/2017	0/0
580	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	12/2017	0/0
581	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	04/2009 -	12/2017	0/0
582	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	04/2008 -	12/2017	0/0
583	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	12/2017	0/0
584	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	12/2017	0/0
585	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	12/2017	0/0
586	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	12/2017	0/0
587	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	12/2017	0/0
588	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	12/2017	0/0
589	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	12/2017	0/0
590	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	12/2017	0/0
591	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	12/2017	0/0
592	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	12/2017	0/0
593	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	12/2017	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(October 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
594	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL	02/2011	1,078.84 -	08/2013 -	12/2017	0/0
595	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI, ODISHA	12/2011	1,047.00 -	06/2014 -	12/2017	0/0
596	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	09/2014 -	12/2017	0/0
597	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH	07/2012	291.36 -	01/2014 -	12/2017	0/0
598	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI, UTTARAKHAND	11/2011	478.51 -	10/2013 -	12/2017	0/0
599	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI, JHARKHAND	12/2012	1,479.00 -	06/2015 -	12/2017	0/0
600	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI, MULTI STATE	10/2012	1,928.22 -	04/2015 -	12/2017	0/0
601	BARSAT-KRISHNANAGAR - [N24000229]NHAI, WEST BENGAL	08/2012	867.00 -	02/2015 -	12/2017	0/0
602	JALANDHAR - AMRITSAR - [N24000351]NHAI, PUNJAB	01/2014	523.85 -	01/2016 -	12/2017	0/0
603	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHAI, MADHYA PRADESH	06/2015	641.02 -	12/2017 -	12/2017	0/0
604	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI, RAJASTHAN	02/2008	1,673.70 -	10/2011 -	12/2017	0/0
605	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI, CHHATTISGARH	02/2013	1,232.00 -	08/2015 -	12/2017	0/0
606	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI, PUNJAB	09/2014	479.00 -	- -	12/2017	0/0
607	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]NHAI, PUNJAB	12/2015	239.23 -	12/2017 -	12/2017	0/0
608	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI, MADHYA PRADESH	03/2015	928.83 -	- -	12/2017	0/0
609	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL	04/2014	1,665.00 -	- -	12/2017	0/0
610	TWO LANING WITH PS OF CHHAPRA - GOPALGANJ - [N24000521]NHAI, BIHAR	08/2015	854.80 -	- -	12/2017	0/0
611	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH, KARNATAKA	01/1991	219.40 -	01/2018 -	01/2018	0/0
612	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL	10/2015	361.15 -	- -	01/2018	0/0
613	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI, MAHARASHTRA	01/2015	972.50 -	07/2017 -	01/2018	0/0
614	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI, HARYANA	07/2015	1,393.00 -	- -	01/2018	0/0
615	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI, MAHARASHTRA	07/2015	1,871.34 -	01/2018 -	01/2018	0/0
616	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, ASSAM	12/2003	160.00 -	05/2008 -	02/2018	0/0
617	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI, HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	02/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(October 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
618	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]NHAI,RAJASTHAN	08/2015	538.08 -	02/2018 -	02/2018	0/0
619	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA	08/2015	723.54 -	02/2018 -	02/2018	0/0
620	JAISALMER - BARMER - [N24000348]NHAI,RAJASTHAN	08/2015	482.27 -	02/2018 -	02/2018	0/0
621	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM	05/2011	176.22 -	02/2018 -	02/2018	0/0
622	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM	11/2014	218.31 -	02/2018 -	02/2018	0/0
623	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	-	02/2018	0/0
624	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	03/2018	0/0
625	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	04/2010 -	03/2018	0/0
626	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	03/2018	0/0
627	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	01/2014 -	03/2018	0/0
628	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	03/2018	0/0
629	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	03/2018	0/0
630	4-LANING OF BRAHMAPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	08/2013 -	03/2018	0/0
631	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	07/2014 -	03/2018	0/0
632	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA	12/2011	942.69 -	06/2014 -	03/2018	0/0
633	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	09/2016 -	03/2018	0/0
634	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI,RAJASTHAN	09/2015	567.51 -	03/2018 -	03/2018	0/0
635	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP,UTTAR PRADESH	06/2015	774.57 -	03/2018 -	03/2018	0/0
636	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH,WEST BENGAL	01/1991	322.00 -	03/2018 -	03/2018	0/0
637	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]NHAI,UTTAR PRADESH	09/2015	768.56 -	03/2018 -	03/2018	0/0
638	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436]NHAI,UTTAR PRADESH	09/2015	664.53 -	03/2018 -	03/2018	0/0
639	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]NHAI,UTTAR PRADESH	09/2015	789.31 -	03/2018 -	03/2018	0/0
640	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,MULTI STATE	09/2015	788.51 -	03/2018 -	03/2018	0/0
641	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH	09/2015	785.78 -	03/2018 -	03/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(October 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
642	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	08/2016 -	03/2018	0/0
643	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH	11/2015	628.45 -	03/2018 -	03/2018	0/0
644	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 -	03/2018 -	03/2018	0/0
645	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTTEE KANON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	03/2018	0/0
646	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	08/2015 -	03/2018	0/0
647	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]NHAI,DELHI	09/2015	771.18 -	-	03/2018	0/0
648	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014 -	04/2018	0/0
649	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA(PKG - 2) - [N24000358]NHAI,HARYANA	10/2015	562.34 -	04/2018 -	04/2018	0/0
650	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	10/2017 -	04/2018	0/0
651	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	04/2018 -	04/2018	0/0
652	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	-	04/2018	0/0
653	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	-	04/2018	0/0
654	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 -	-	04/2018	0/0
655	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR	08/2015	516.13 -	-	04/2018	0/0
656	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MORTH,ODISHA	01/2015	326.63 327.00	04/2018 -	04/2018	0/0
657	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA	01/1991	229.41 265.35	05/2018 -	05/2018	0/0
658	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	-	05/2018	0/0
659	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	-	05/2018	0/0
660	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	-	05/2018	0/0
661	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	-	05/2018	0/0
662	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA	11/2015	867.66 -	-	05/2018	0/0
663	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	-	05/2018	0/0
664	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	-	05/2018	0/0
665	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA (PKG - 1) - [N24000597]NHAI,HARYANA	05/2015	600.85 -	-	05/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(October 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
666	PATNA-MUZZAFFARPUR - [N24000165]NHAI, BIHAR	08/2010	671.30 -	02/2013 -	06/2018	0/0
667	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH, RAJASTHAN	12/2015	621.43 -	06/2018 -	06/2018	0/0
668	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI, TAMIL NADU	06/2015	563.92 -	12/2017 -	06/2018	0/0
669	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI, UTTAR PRADESH	05/2015	261.09 -	05/2017 -	06/2018	0/0
670	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI, TAMIL NADU	11/2014	563.92 -	11/2016 -	06/2018	0/0
671	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL, ASSAM	12/2015	223.30 -	06/2018 -	06/2018	0/0
672	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI, HARYANA	12/2015	602.95 -	06/2016 -	06/2018	0/0
673	4-LANING OF GHAGHRA BRIDGE TO VARANASI (PACKAGE -I) - [N24000460]NHAI, UTTAR PRADESH	12/2015	611.65 -	06/2016 -	06/2018	0/0
674	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL	12/2015	1,083.00 -	06/2018 -	06/2018	0/0
675	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP, MADHYA PRADESH	12/2015	927.54 -	06/2018 -	06/2018	0/0
676	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI, UTTAR PRADESH	01/2016	815.28 -	06/2018 -	06/2018	0/0
677	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI, UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	06/2018	0/0
678	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI, UTTAR PRADESH	06/2016	667.00 -	07/2018 -	06/2018	0/0
679	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI, UTTAR PRADESH	12/2015	667.00 -	06/2018 -	06/2018	0/0
680	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI, KERALA	04/2016	804.97 -	- -	06/2018	0/0
681	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI, HARYANA	01/2016	574.28 -	07/2018 -	07/2018	0/0
682	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]NHAI, MADHYA PRADESH	01/2016	830.36 -	07/2018 -	07/2018	0/0
683	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR-HYDERABAD SECTION NS-62 - [N24000542]NHAI, MAHARASHTRA	03/2016	197.69 -	- -	07/2018	0/0
684	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI, TAMIL NADU	02/2016	641.17 -	- -	07/2018	0/0
685	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR-HYDERABAD SECTION NS-60 - [N24000561]NHAI, MAHARASHTRA	03/2016	244.00 -	- -	07/2018	0/0
686	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI, UTTARAKHAND	11/2012	605.84 -	- -	07/2018	0/0
687	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI, TAMIL NADU	03/2016	641.17 -	07/2016 -	07/2018	0/0
688	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI, KARNATAKA	03/2015	1,388.00 -	- -	08/2018	0/0
689	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI, TAMIL NADU	02/2016	707.82 -	- -	08/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(October 2017)		
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
690	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	- -	08/2018	0/0
691	FOUR LANNING OF CHICHA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL	09/2016	767.03 -	- -	08/2018	0/0
692	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI, RAJASTHAN	07/2016	331.46 -	- -	10/2018	0/0
693	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI, TELANGANA	12/2015	1,423.96 -	- -	11/2018	0/0
694	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI, ANDHRA PRADESH	01/2016	1,134.97 -	- -	11/2018	0/0
695	CONSTRUCTION OF ROB - FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI, WEST BENGAL	03/2016	229.37 -	- -	11/2018	0/0
696	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH, ODISHA	06/2016	157.30 157.00	06/2018 -	11/2018	0/0
697	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHAI, ASSAM	12/2015	289.99 -	12/2018 -	12/2018	0/0
698	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI, JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	12/2018	0/0
699	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI, UTTAR PRADESH	07/2015	1,657.20 -	- -	01/2019	0/0
700	FOUR LANING OF BIAORA - DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI, MADHYA PRADESH	06/2015	1,583.79 -	- -	01/2019	0/0
701	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI, RAJASTHAN	08/2016	320.30 -	- -	01/2019	0/0
702	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI, MADHYA PRADESH	08/2016	227.49 -	- -	01/2019	0/0
703	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI, HIMACHAL PRADESH	02/2016	273.20 -	- -	02/2019	0/0
704	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	03/2019	0/0
705	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI, MAHARASHTRA	12/2015	649.50 -	- -	03/2019	0/0
706	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI, MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	03/2019	0/0
707	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI, JHARKHAND	02/2016	997.15 -	- -	03/2019	0/0
708	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI, KARNATAKA	08/2016	1,167.42 -	- -	03/2019	0/0
709	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI, MAHARASHTRA	11/2016	400.25 -	- -	03/2019	0/0
710	4-LANNING OF KODEBAD-DHMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI, MAHARASHTRA	11/2016	446.17 -	- -	03/2019	0/0
711	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI, HARYANA	07/2015	2,128.72 -	- -	04/2019	0/0
712	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI, BIHAR	12/2015	1,041.10 -	- -	04/2019	0/0
713	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI, PUNJAB	10/2015	447.29 -	12/2017 -	04/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(October 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
714	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI, BIHAR	08/2015	399.54 -	- -	04/2019	0/0
715	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI, UTTAR PRADESH	03/2016	676.73 -	- -	04/2019	0/0
716	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI, UTTAR PRADESH	03/2016	1,587.49 -	- -	04/2019	0/0
717	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI, UTTAR PRADESH	03/2016	899.00 -	- -	04/2019	0/0
718	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI, UTTAR PRADESH	08/2016	2,016.00 -	- -	04/2019	0/0
719	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI, KARNATAKA	08/2016	1,664.20 -	- -	04/2019	0/0
720	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI, MAHARASHTRA	07/2015	2,288.18 -	- -	05/2019	0/0
721	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI, MAHARASHTRA	07/2015	1,885.74 -	- -	05/2019	0/0
722	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]NHAI, UTTAR PRADESH	01/2016	701.12 -	- -	05/2019	0/0
723	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI, HARYANA	08/2016	248.97 -	- -	05/2019	0/0
724	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI, HARYANA	09/2016	1,004.67 -	- -	05/2019	0/0
725	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI, MAHARASHTRA	01/2017	244.90 -	- -	05/2019	0/0
726	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI, MAHARASHTRA	03/2017	296.19 -	03/2020 -	05/2019	0/0
727	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI, JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	06/2019	0/0
728	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI, UTTAR PRADESH	01/2016	1,081.57 -	- -	06/2019	0/0
729	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI, RAJASTHAN	06/2016	637.18 -	06/2019 -	06/2019	0/0
730	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI, RAJASTHAN	06/2016	763.23 -	06/2019 -	06/2019	0/0
731	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI, RAJASTHAN	06/2016	649.00 -	06/2019 -	06/2019	0/0
732	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI, MAHARASHTRA	03/2016	546.00 -	- -	07/2019	0/0
733	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI, MAHARASHTRA	03/2016	591.66 -	- -	07/2019	0/0
734	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL, NAGALAND	03/2016	373.07 -	08/2016 -	08/2019	0/0
735	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL, NAGALAND	03/2016	396.52 -	08/2016 -	08/2019	0/0
736	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL, NAGALAND	03/2016	429.52 -	08/2016 -	08/2019	0/0
737	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199 (DESIGN CHAINAGE) - [N24000600]NHAI, PUNJAB	08/2016	1,388.34 -	- -	09/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(October 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
738	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL, ARUNACHAL PRADESH	12/2016	138.93 155.00	01/2017 -	01/2020	0/0
739	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI, MAHARASHTRA	02/2017	904.16 -	02/2020 -	02/2020	0/0
740	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI, UTTAR PRADESH	03/2017	1,373.28 -	03/2020 -	03/2020	0/0
741	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI, UTTAR PRADESH	03/2017	1,184.71 -	03/2020 -	03/2020	0/0
742	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI, MAHARASHTRA	03/2017	247.02 -	03/2020 -	03/2020	0/0
743	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI, MAHARASHTRA	03/2017	744.64 -	03/2020 -	03/2020	0/0
744	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI, MAHARASHTRA	03/2017	1,030.44 -	03/2020 -	03/2020	0/0
745	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI, MAHARASHTRA	03/2017	988.34 -	03/2020 -	03/2020	0/0
746	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI, MAHARASHTRA	03/2017	1,098.06 -	03/2020 -	03/2020	0/0
747	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI, PUNJAB	03/2017	754.54 -	03/2020 -	03/2020	0/0
748	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI, UTTAR PRADESH	03/2017	1,989.00 -	03/2020 -	03/2020	0/0
749	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI, HARYANA	03/2017	639.79 -	03/2020 -	03/2020	0/0
750	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI, BIHAR	03/2017	672.89 -	03/2020 -	03/2020	0/0
751	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI, BIHAR	03/2017	235.48 -	03/2020 -	03/2020	0/0
752	REHABILITATION AND UPGRADE OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]NHAI, ANDHRA PRADESH	03/2017	648.32 -	03/2020 -	03/2020	0/0
753	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI, ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	03/2020	0/0
754	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]NHAI, JHARKHAND	03/2017	165.50 -	03/2020 -	03/2020	0/0
755	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI, JHARKHAND	03/2017	239.68 -	03/2020 -	03/2020	0/0
756	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI, UTTAR PRADESH	03/2017	2,064.99 -	03/2020 -	03/2020	0/0
757	SIX LANING AND STRENGTHENING OF KM 340+000 TO KM 403+400 OF HUBLI-HAVERI SECTION OF NH-48 (OLD NH-4) - [N24000673]NHAI, KARNATAKA	03/2017	985.41 -	03/2020 -	03/2020	0/0
758	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI, KARNATAKA	03/2017	831.58 -	03/2020 -	03/2020	0/0
759	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI, KARNATAKA	03/2017	993.16 -	03/2020 -	03/2020	0/0
760	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI, RAJASTHAN	04/2017	894.00 -	04/2020 -	04/2020	0/0
761	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI, HIMACHAL PRADESH	06/2017	2,485.93 -	06/2020 -	06/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(October 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
762	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI, GUJARAT	06/2017	1,958.88 -	06/2020 -	06/2020	0/0
763	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, RAJASTHAN	12/2003	275.00 -	02/2010 -	-	0/0
764	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, MULTI STATE	12/2003	604.00 -	12/2009 -	-	0/0
765	TALEGAON-AMRAVATI - [N24000140]NHAI, MAHARASHTRA	11/2009	567.00 -	11/2013 -	-	0/0
766	NASHRI- CHANANI - [N24000162]NHAI, JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-	0/0
767	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI, TAMIL NADU	06/2011	600.00 -	06/2013 -	-	0/0
768	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT	01/2011	953.88 -	07/2013 -	-	0/0
769	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, BIHAR	05/2011	664.00 -	02/2014 -	-	0/0
770	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, BIHAR	10/2011	375.09 -	04/2014 -	-	0/0
771	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI, TAMIL NADU	04/2012	624.00 -	04/2014 -	-	0/0
772	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI, RAJASTHAN	03/2014	240.10 -	03/2016 -	-	0/0
773	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735 (IBRAHIMPATNAM TO CHANDR - [N24000273]MORTH, ANDHRA PRADESH	07/2015	314.43 -	- -	-	0/0
774	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH, MAHARASHTRA	10/2015	289.60 -	- -	-	0/0
775	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH, MAHARASHTRA	12/2011	156.26 227.31	- 03/2013	-	0/0
776	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD, CHHATISGARH	12/2010	169.26 -	12/2012 -	-	0/0
777	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD, CHHATISGARH	12/2014	394.20 -	- -	-	0/0
778	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD, CHHATISGARH	11/2015	485.44 -	12/2015 -	-	0/0
779	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110 (ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH, CHHATISGARH	03/2015	422.34 -	- -	-	0/0
780	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000 (ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD, PUNJAB	03/2015	435.90 -	- -	-	0/0
781	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD, PUNJAB	01/2015	279.68 -	- -	-	0/0
782	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71 (NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD, PUNJAB	11/2014	463.65 546.00	- -	-	0/0
783	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71 (NEW NH-52) FROM - [N24000292]PWD, PUNJAB	11/2014	573.96 605.00	- -	-	0/0
784	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150 (KATHIPUDI TO START OF K - [N24000293]MORTH, ANDHRA PRADESH	10/2015	480.21 -	- -	-	0/0
785	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH, RAJASTHAN	10/2014	269.22 -	01/2015 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(October 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
786	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-	0/0
787	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-	0/0
788	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-	0/0
789	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-	0/0
790	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	03/2011 -	-	0/0
791	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-	0/0
792	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	-	0/0
793	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-	0/0
794	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 -	-	0/0
795	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 -	08/2013 -	-	0/0
796	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 -	08/2013 -	-	0/0
797	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 -	02/2013 -	-	0/0
798	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-	0/0
799	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 268.92	08/2015 -	-	0/0
800	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-	0/0
801	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH	03/2015	629.74 -	- -	-	0/0
802	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-	0/0
803	PADI - DAHOD - [N24000353]NHAI,RAJASTHAN	11/2014	279.14 -	05/2017 -	-	0/0
804	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]NHAI,RAJASTHAN	10/2014	264.72 -	04/2017 -	-	0/0
805	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	-	0/0
806	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH	06/2014	301.04 -	01/2016 -	-	0/0
807	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB	02/2015	483.38 -	- -	-	0/0
808	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB	02/2015	616.36 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(October 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
809	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB	02/2015	486.74 -	- -	-	0/0
810	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	- -	-	0/0
811	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-	0/0
812	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB	03/2015	312.79 -	- -	-	0/0
813	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOLA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB	07/2014	319.80 -	- -	-	0/0
814	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	- -	-	0/0
815	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH	01/2011	264.16 -	- -	-	0/0
816	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	-	0/0
817	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	- -	-	0/0
818	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	- -	-	0/0
819	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB	12/2015	578.38 -	- -	-	0/0
820	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE	03/2015	789.83 -	- -	-	0/0
821	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	-	0/0
822	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	-	0/0
823	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-	0/0
824	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-	0/0
825	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	- -	-	0/0
826	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	- -	-	0/0
827	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA	09/2005	168.00 -	06/2006 -	-	0/0
828	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-	0/0
829	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	- -	-	0/0
830	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	- -	-	0/0
831	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- -	-	0/0
832	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(October 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
833	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	- -	-	0/0
834	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-	0/0
835	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98 -	- -	-	0/0
836	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-	0/0
837	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-	0/0
838	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	-	0/0
839	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB	06/2015	899.21 -	- -	-	0/0
840	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-	0/0
841	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-	0/0
842	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-	0/0
843	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-	0/0
844	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR	10/2014	377.64 -	03/2014 -	-	0/0
845	MEERUT-BULANDSHAHAH - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	- -	-	0/0
846	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-	0/0
847	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-	0/0
848	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	- -	-	0/0
849	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	- -	-	0/0
850	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	- -	-	0/0
851	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	- -	-	0/0
852	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	- -	-	0/0
853	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	-	0/0
854	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	- -	-	0/0
855	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	- -	-	0/0
856	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(October 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
857	FOUR LANING OF TALAJA – MAHUA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT	05/2016	834.64 -	- -	-	0/0
858	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	- -	-	0/0
859	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	- -	-	0/0
860	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	-	0/0
861	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	- -	-	0/0
862	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR	01/2013	322.01 -	08/2014 -	-	0/0
863	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR	11/2013	683.83 -	07/2016 -	-	0/0
864	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR	02/2014	665.50 -	07/2016 -	-	0/0
865	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR	02/2016	178.85 -	05/2016 -	-	0/0
866	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR	02/2016	553.30 -	05/2016 -	-	0/0
867	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-	0/0
868	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR	08/2015	288.24 -	11/2015 -	-	0/0
869	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA	03/2016	1,142.62 -	- -	-	0/0
870	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA	03/2016	1,101.58 -	- -	-	0/0
871	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	-	0/0
872	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 -	- -	-	0/0
873	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	-	0/0
874	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	- -	-	0/0
875	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA	05/2014	720.69 -	- -	-	0/0
876	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 -	- -	-	0/0
877	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	-	0/0
878	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-	0/0
879	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH	04/2016	245.79 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(October 2017)		
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
880	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACHAL PRADESH - [N24000618]NHIDCL,ARUNACHAL PRADESH	11/2015	434.06 -	- -	-	0/0
881	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN	09/2016	1,239.82 -	- -	-	0/0
882	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 -	- -	-	0/0
883	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	- -	-	0/0
884	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	- -	-	0/0
885	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA	11/2016	1,071.61 -	- -	-	0/0
886	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA	11/2016	1,064.88 -	- -	-	0/0
887	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	- -	-	0/0
888	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	- -	-	0/0
889	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	- -	-	0/0
890	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT	12/2016	417.19 -	- -	-	0/0
891	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASTHAN(PACKAGE - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	- -	-	0/0
892	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	-	0/0
893	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-	0/0
894	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	- -	-	0/0
895	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	-	0/0
896	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH	01/2017	1,253.10 -	03/2017 -	-	0/0
897	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH	03/2017	284.09 -	04/2017 -	-	0/0
898	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH	02/2017	195.23 -	04/2017 -	-	0/0
899	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH	02/2017	203.36 -	04/2017 -	-	0/0
900	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH	01/2017	194.66 -	04/2017 -	-	0/0
901	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH	02/2017	168.32 -	04/2017 -	-	0/0
902	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 -	04/2017 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(October 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
903	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH	02/2017	216.71 -	04/2017 -	-	0/0
904	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH	02/2017	167.28 -	04/2017 -	-	0/0
905	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND	02/2017	507.68 -	04/2017 -	-	0/0
906	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH	01/2017	198.22 -	04/2017 -	-	0/0
907	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	03/2013 -	06/2017	0/0
908	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH	12/2015	291.05 -	- -	-	0/0
909	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	-	0/0
910	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 -	03/2020 -	-	0/0
	Total		3,05,443.93 -			0/0
	<u>SHIPPING AND PORTS</u>					
911	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	03/2006 -	12/2017	0/0
912	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068]KPL,TAMIL NADU	09/2015	210.00 -	01/2018 -	01/2018	0/0
913	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 -	12/2010 -	12/2018	0/0
914	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-	0/0
915	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 -	04/2009 -	-	0/0
	Total		3,399.46 -			0/0
	<u>TELECOMMUNICATIONS</u>					
916	MAHARASHTRA NODAL (LOT 1) - [N26000107]BSNL,MAHARASHTRA	08/2017	156.00 -	04/2018 -	04/2018	0/0
917	MAHARASHTRA CORE (LOT1) - [N26000108]BSNL,MAHARASHTRA	08/2017	156.77 -	04/2018 -	04/2018	0/0
918	GUJARAT ACCESS (LOT 1) - [N26000111]BSNL,GUJARAT	09/2017	171.54 -	04/2018 -	04/2018	0/0
919	MAHARASHTRA ACESS (LOT 1) - [N26000109]BSNL,MAHARASHTRA	08/2017	213.00 -	05/2018 -	05/2018	0/0
920	MADHYA PRADESH ACCESS (LOT1) - [N26000110]BSNL,MAHARASHTRA	08/2017	215.30 -	05/2018 -	05/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above

(October 2017)

			Date of Commissioning (Month/Year)			
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
921	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00	07/2015	06/2019	0/0
922	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI	06/2016	418.26	06/2017	-	0/0
	Total		14,664.87			0/0
	<u>URBAN DEVELOPMENT</u>					
923	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00	03/2016	12/2016	0/0
924	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72	09/2016	11/2017	0/0
925	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87	12/2015	12/2017	0/0
926	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN - [N28000091]CPWD,RAJASTHAN	08/2014	350.02	03/2015	12/2017	0/0
927	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER - [N28000093]CPWD,KERALA	07/2015	154.00	11/2015	12/2017	0/0
928	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30	12/2015	03/2018	0/0
929	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU	06/2016	3,770.00	03/2018	03/2018	0/0
930	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83	11/2014	10/2018	0/0
931	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH	01/2016	6,928.00	03/2019	03/2019	0/0
932	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL	10/2014	162.88	04/2018	06/2019	0/0
933	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26	12/2013	10/2019	0/0
934	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79	07/2017	12/2019	0/0
935	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00	03/2018	12/2019	0/0
936	RESIDENTIAL QUATERS FOR HAL,BANGLORE - [N28000103]CPWD,KARNATAKA	12/2016	246.31	02/2020	02/2020	0/0
937	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA	02/2014	26,405.14	02/2019	03/2020	0/0
938	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21	10/2019	03/2020	0/0
939	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH	08/2007	246.90	-	-	0/0
940	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00	01/2015	-	0/0
941	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18	06/2017	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above				(October 2017)		
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	Total		1,17,352.41 -			0/0
	Grand Total		10,07,811.49			0/0

List of Projects Ahead of Schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(October 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>PETROLEUM</u>						
1	PARADIP HYDERABAD PIPELINE - [N16000194]	1/2015	2,321.00 -	2,321.00	55.55	12/2020 -	08/2020
2	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216]	1/2016	247.52 -	247.52	53.50	02/2019 -	12/2018
3	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP - [N16000226]	2/2016	356.00 -	356.00	72.34	05/2019 -	12/2018
4	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]	9/2015	4,199.00 -	4,199.00	194.97	03/2020 -	07/2019
5	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL [N16000252]	5/2016	664.00 -	664.00	147.71	12/2020 -	02/2020
	Total		7,787.52 -	7,787.52	524.07		
	<u>POWER</u>						
6	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII [N18000159]	2/2014	908.08 969.97	969.97	722.47	06/2016 02/2018	11/2017
7	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) [N18000207]	1/2016	244.19 -	244.19	116.50	07/2018 -	10/2017
8	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]	1/2016	162.11 -	162.11	115.28	05/2018 -	12/2017
	Total		1,314.38 -	1,376.27	954.25		
	<u>RAILWAYS</u>						
9	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]	4/2015	1,172.92 -	1,172.92	74.32	03/2021 -	03/2020
	Total		1,172.92 -	1,172.92	74.32		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
10	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]	6/2016	667.00 -	667.00	122.01	07/2018 -	06/2018
11	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]	3/2017	296.19 -	254.00	-	03/2020 -	05/2019
	Total		963.19 -	921.00	122.01		
	Grand Total		11,238.01	11,257.71	1,674.65		

List of Projects on schedule w.r.t. Latest Schedule

Annexure - XII

Costing Rs.150 Crore and above						(October 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
1	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	9/2008	152.43 -	459.49	80.16	03/2015 03/2020	03/2020
2	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	271.12	03/2022 -	03/2022
3	BATURA OCP (2.0 MTY) - [N06000049]	8/2015	1,186.64 -	1,186.64	58.50	03/2023 -	03/2023
4	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	5.73	03/2023 -	03/2023
5	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	28.74	03/2022 -	03/2022
6	MALACHUA OPENCAST PROJECT - [N06000139]	10/2015	488.33 -	488.33	1.06	03/2023 -	03/2023
7	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	277.65	.13	03/2021 -	03/2021
8	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	7.61	03/2022 -	03/2022
9	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	47.23	03/2020 -	03/2020
10	GOKUL - [N06000120]	11/2014	267.67 -	267.67	204.35	03/2018 -	03/2018
11	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	138.85	03/2021 -	03/2021
12	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	362.59	03/2020 -	03/2020
13	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	369.08	03/2021 -	03/2021
14	KULDA EXPN OC. (5.00 MTY) - [N06000115]	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
15	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]	5/2014	337.66 -	337.66	29.74	03/2019 -	03/2019
16	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	682.14	03/2026 -	03/2026
17	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]	5/2014	479.15 -	479.15	20.80	03/2019 -	03/2019
18	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	4.57	03/2021 -	03/2021
19	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]	3/2015	522.45 -	522.45	5.65	09/2019 -	09/2019
20	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	174.80	03/2020 -	03/2020
21	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	430.95	03/2018 -	03/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(October 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
22	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	1,369.37	03/2023 -	03/2023
23	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	.57	03/2023 -	03/2023
24	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	38.29	03/2020 -	03/2020
25	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
26	ADASA UG TO OC - [N06000133]	8/2015	288.90 -	288.90	-	03/2023 -	03/2023
27	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	229.90	03/2025 -	03/2025
28	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	1,123.80	11/2021 -	11/2021
29	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	71.98	03/2021 -	03/2021
30	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	69.58	03/2020 -	03/2020
31	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	5/2015	397.09 -	442.42	25.07	03/2019 -	03/2019
32	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	295.56	86.17	03/2019 -	03/2019
33	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	34.39	03/2021 -	03/2021
34	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	114.37	03/2021 -	03/2021
35	AMERA OC RCE - [N06000123]	2/2015	335.97 -	335.97	48.78	03/2018 -	03/2018
36	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
37	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	75.98	03/2026 -	03/2026
38	DHANKASA UG (1.00 MTY) - [N06000155]	9/2016	458.07 -	458.07	-	03/2022 -	03/2022
39	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	319.76	.04	03/2022 -	03/2022
40	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]	7/2016	409.87 -	409.87	12.08	03/2022 -	03/2022
41	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]	2/2016	198.68 -	198.68	39.89	03/2019 -	03/2019
42	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]	3/2016	869.44 -	869.44	111.56	03/2021 -	03/2021
43	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]	12/2015	477.65 -	477.65	-	03/2020 -	03/2020
44	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]	3/2015	513.63 -	513.63	167.04	12/2019 -	12/2019
45	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	175.44	03/2020 -	03/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(October 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
46	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	6/2011	5,907.11 -	5,907.11	4,834.48	12/2015 04/2018	04/2018
47	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]	6/2010	11,816.40 -	11,816.40	2,519.20	03/2023 -	03/2023
48	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	7.72	03/2020 -	03/2020
49	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
50	BHATADI EXPANSION OC MINE - [N06000150]	2/2016	304.52 -	304.52	125.81	03/2019 -	03/2019
51	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]	4/2013	1,458.17 -	709.06	302.65	06/2015 09/2019	09/2019
	Total		72,701.13 -	72,305.21	14,507.96		
	<u>DEFENCE PRODUCTION</u>						
52	CONSTRUCTION WORKS PHASE 4 - [N39000001]	12/2016	167.69 168.00	172.99	24.16	05/2018 -	05/2018
53	CONSTRUCTION WORKS PHASE 3B - [N39000002]	12/2016	285.95 286.00	296.05	31.52	08/2020 -	08/2020
	Total		453.64 -	469.04	55.68		
	<u>FERTILISERS</u>						
54	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	82.72	11/2016 04/2019	04/2019
55	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]	2/2016	482.85 -	494.00	400.18	12/2017 -	12/2017
	Total		680.64 -	703.44	482.90		
	<u>HEALTH AND FAMILY WELFARE</u>						
56	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	9/2014	505.58 -	505.58	238.00	03/2018 -	03/2018
57	CNCI KOLKATA WEST BENGAL - [N21000015]	8/2016	244.00 -	244.00	72.00	09/2018 -	09/2018
58	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]	8/2017	355.15 -	355.15	7.10	03/2019 -	03/2019
59	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	8/2017	272.19 -	272.19	5.45	03/2019 -	03/2019
60	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]	8/2017	274.19 -	274.19	5.48	03/2019 -	03/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(October 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
61	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA - [N21000014]	7/2016	312.99 -	312.99	128.00	08/2018 -	08/2018
62	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]	10/2016	363.99 -	363.99	14.00	05/2018 08/2019	08/2019
	Total		2,328.09 -	2,328.09	470.03		
	<u>MINES</u>						
63	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	5,540.00 -	5,540.00	23.84	04/2021 04/2021	04/2021
64	UTKAL D AND E COAL BLOCK - [N10000011]	5/2016	534.00 -	534.00	192.54	01/2020 01/2020	01/2020
	Total		6,074.00 -	6,074.00	216.38		
	<u>PETROLEUM</u>						
65	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]	3/2009	2,465.15 -	2,378.89	2,060.68	03/2013 09/2018	09/2018
66	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) [N16000084]	6/2007	736.65 -	571.47	542.29	09/2011 06/2019	06/2019
67	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]	5/2013	711.00 -	711.00	11.12	06/2020 -	06/2020
68	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	5/2013	4,124.35 -	5,637.00	3,947.52	04/2016 12/2017	12/2017
69	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]	5/2016	406.00 -	406.00	.50	10/2020 -	10/2020
70	BSVI UPGRADATION - [N16000257]	9/2016	1,810.00 1,810.00	1,810.00	52.96	12/2019 -	12/2019
71	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]	10/2015	135.00 171.00	170.70	81.39	03/2019 -	03/2019
72	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]	5/2015	224.00 207.00	207.25	42.14	04/2019 -	04/2019
73	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]	9/2015	324.00 -	324.00	1.48	06/2020 -	06/2020
74	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	5/2016	4,497.00 -	4,497.00	24.07	12/2018 -	12/2018
75	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]	4/2016	1,021.00 -	1,021.00	6.35	12/2020 -	12/2020
76	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]	2/2016	151.00 -	151.00	-	09/2019 -	09/2019
77	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	72.56	08/2021 -	08/2021
78	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	7/2016	249.85 250.00	244.70	-	05/2020 05/2020	05/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(October 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
79	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]	5/2016	429.00 -	429.00	39.02	01/2019 -	01/2019
80	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]	5/2016	261.00 -	261.00	.05	01/2021 -	01/2021
81	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	3/2017	1,828.00 -	1,828.00	.93	12/2020 -	12/2020
82	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]	3/2017	3,212.00 -	3,212.00	1.47	12/2020 -	12/2020
83	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]	3/2017	2,250.00 -	2,250.00	4.87	12/2019 -	12/2019
84	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	3/2017	2,253.00 -	2,253.00	12.88	12/2019 -	12/2019
85	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]	7/2015	2,881.40 -	2,881.40	9.98	12/2019 -	12/2019
86	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]	7/2014	247.00 -	247.00	-	03/2021 -	03/2021
87	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]	2/2017	968.61 -	968.61	-	11/2019 -	11/2019
88	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]	2/2017	511.30 -	511.30	-	11/2019 -	11/2019
89	DEVELOPMENT OF B-147 FIELD - [N16000292]	2/2017	546.15 -	546.15	-	11/2019 -	11/2019
90	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY - [N16000290]	1/2017	474.15 -	474.15	110.96	05/2019 -	05/2019
91	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]	7/2017	268.79 -	268.79	1.21	07/2022 -	07/2022
92	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	287.49	14.70	04/2022 -	04/2022
93	AUGMENTATION OF CTMPL - [N16000286]	12/2016	228.00 -	228.00	-	06/2020 -	06/2020
94	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]	9/2016	208.35 -	208.35	16.93	07/2020 -	07/2020
95	LPG BP PROJECT KHORDHA - [N16000283]	12/2016	161.59 -	161.59	28.80	12/2019 -	12/2019
96	SITARGANJ LPG PROJECT - [N16000282]	2/2017	160.10 -	160.10	20.22	02/2020 -	02/2020
97	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]	4/2017	420.76 -	420.76	-	09/2018 09/2018	09/2018
98	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	1,162.56	196.84	03/2026 03/2026	03/2026

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(October 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
99	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]	1/2015	342.00 -	342.00	-	03/2021 -	03/2021
100	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]	5/2016	348.00 -	348.00	.05	01/2021 -	01/2021
101	ADDITIONAL FACILITIES AT MANMAD FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]	5/2016	212.00 -	212.00	.08	01/2021 -	01/2021
102	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT KOCHI REFINERY - [N16000264]	5/2015	337.06 -	337.06	20.75	08/2018 -	08/2018
103	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]	2/2016	3,313.00 -	3,313.00	65.92	02/2020 -	02/2020
104	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY - [N16000262]	5/2015	193.40 -	193.40	8.55	01/2019 -	01/2019
105	MMPL PIPELINE REROUTING PROJECT - [N16000261]	4/2013	449.58 -	449.58	97.27	12/2019 -	12/2019
106	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]	9/2016	571.66 -	571.66	-	12/2019 -	12/2019
107	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]	7/2015	822.66 -	822.66	223.14	11/2018 -	11/2018
108	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]	3/2016	34,012.00 -	34,012.00	253.97	06/2020 06/2020	06/2020
109	SONAMURA GGS AND PIPELINE PROJECT (PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A - [N16000246]	5/2016	215.38 -	215.38	162.34	06/2017 01/2018	01/2018
110	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	2/2015	749.00 -	749.00	504.66	02/2020 -	02/2020
111	DIESEL HYDROTREATOR - [N16000207]	7/2015	1,031.37 -	1,031.37	305.91	01/2018 -	01/2018
112	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]	3/2015	3,957.00 -	3,397.00	1,399.57	12/2018 -	12/2018
113	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]	8/2015	2,818.88 -	2,818.88	338.56	03/2019 05/2020	05/2020
114	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]	2/2015	2,899.93 -	2,098.43	1,237.43	05/2017 05/2018	05/2018
115	GAMJI REDEVELOPMENT PROJECT - [N16000202]	5/2015	1,671.22 -	567.22	347.69	11/2019 12/2018	12/2018
116	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]	3/2014	238.50 -	238.50	167.48	03/2017 10/2017	10/2017
117	DAMAN DEVELOPMENT PROJECT - [N16000198]	8/2014	6,086.08 -	5,479.75	2,148.82	05/2019 10/2019	10/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(October 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
118	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]	11/2014	6,068.80 -	5,296.93	4,250.08	04/2019 03/2019	03/2019
119	PARADIP LPG IMPORT FACILITY - [N16000196]	1/2015	690.00 -	690.00	133.80	07/2018 06/2020	06/2020
120	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]	2/2015	890.00 -	887.00	223.15	10/2019 -	10/2019
121	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	1/2015	1,823.00 -	1,823.00	41.75	12/2020 -	12/2020
122	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	6/2014	5,706.47 -	5,813.25	5,554.21	05/2017 05/2018	05/2018
123	AURAIYA PHULPUR PIPELINE PROJECT - [N16000231]	7/2015	1,427.94 -	1,427.94	434.76	12/2018 -	12/2018
124	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29 -	4,588.29	927.73	08/2018 05/2019	05/2019
125	PALAKKAD LPG PLANT - [N16000225]	2/2015	184.00 -	184.00	81.68	12/2017 -	12/2017
126	ENNORE TERMINAL - [N16000224]	8/2014	393.00 -	393.00	211.60	04/2018 -	04/2018
127	HALDIA LPG IMPORT FACILITY - [N16000223]	3/2015	694.00 -	694.00	197.10	10/2018 -	10/2018
128	NEW 250 TMTA LPG PLANT AT PANAGARH - [N16000222]	8/2014	190.45 -	190.45	130.15	09/2017 03/2018	03/2018
129	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]	3/2009	181.02 -	173.28	127.44	01/2017 03/2018	03/2018
130	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	864.69	04/2018 04/2018	04/2018
131	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]	1/2015	4,619.94 -	3,961.54	3,424.59	12/2017 03/2019	03/2019
132	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]	2/2016	2,582.00 -	2,582.00	250.76	11/2019 -	11/2019
133	RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB,HARYANA) - [N16000242]	11/2016	230.00 -	230.00	13.37	02/2019 -	02/2019
134	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	658.62 -	910.23	5.22	03/2023 03/2022	03/2022
135	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]	9/2016	1,879.00 -	1,879.00	209.30	06/2020 -	06/2020
136	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]	9/2016	407.00 -	407.00	30.61	09/2019 -	09/2019
137	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]	6/2016	423.00 -	423.00	91.45	08/2019 -	08/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(October 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
138	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,928.00 -	20,928.00	540.49	07/2020 -	07/2020
139	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]	4/2016	327.78 -	200.00	15.19	04/2018 -	04/2018
140	ANKLESHWAR BARODA PIPELINE PROJECT - [N16000232]	7/2014	199.95 -	199.95	121.90	03/2018 -	03/2018
141	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]	11/2014	195.63 -	187.10	139.30	09/2018 09/2018	09/2018
142	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	723.40	394.90	10/2014 03/2018	03/2018
143	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]	2/2011	913.00 -	1,330.00	1,036.41	06/2018 -	06/2018
144	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]	4/2012	600.17 -	600.17	657.00	12/2014 03/2018	03/2018
145	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]	3/2012	2,592.17 -	2,592.17	2,040.89	05/2014 05/2018	05/2018
146	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	1,650.87	03/2015 03/2018	03/2018
147	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	3/2011	861.79 -	1,256.72	1,170.49	05/2013 12/2017	12/2017
148	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]	6/2010	202.94 -	330.35	3.14	01/2014 11/2019	11/2019
149	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00 -	3,150.00	1,308.04	09/2017 12/2018	12/2018
150	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]	3/2014	3,076.00 -	4,190.00	2,125.22	09/2017 06/2018	06/2018
151	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]	9/2011	202.25 -	160.16	106.98	07/2016 06/2018	06/2018
	Total		1,70,274.31 -	1,70,345.92	43,098.37		
	POWER						
152	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]	10/2008	4,824.12 -	5,071.94	4,484.38	10/2012 02/2018	02/2018
153	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	2/2009	11,130.19 -	13,762.80	12,558.71	08/2013 12/2017	12/2017
154	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]	1/2014	374.63 -	374.63	116.52	04/2016 12/2017	12/2017
155	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]	2/2014	539.82 -	539.82	388.72	06/2016 02/2018	02/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(October 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
156	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]	2/2010	2,144.00 -	2,932.88	2,566.17	12/2012 02/2018	02/2018
157	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]	8/2017	1,931.39 -	1,931.39	6.91	02/2020 -	02/2020
158	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]	5/2017	445.89 -	445.89	-	02/2019 -	02/2019
159	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]	5/2017	186.17 -	186.17	7.74	07/2019 -	07/2019
160	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]	5/2017	175.64 -	175.64	4.99	09/2018 -	09/2018
161	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	3/2017	3,500.00 3,500.00	3,500.00	55.00	07/2020 -	07/2020
162	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]	12/2015	3,654.00 -	3,654.00	951.00	04/2019 -	04/2019
163	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V - [N18000256]	2/2015	1,750.00 -	1,750.00	458.00	06/2018 -	06/2018
164	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-B - [N18000255]	4/2015	2,225.00 2,225.00	2,225.00	869.00	01/2018 -	01/2018
165	AMELIA COAL MINE - [N18000252]	1/2017	2,104.21 -	2,104.21	40.37	09/2020 -	09/2020
166	50 MW SOLAR POWER PROJECT - [N18000251]	9/2017	287.48 -	287.48	28.25	03/2018 -	03/2018
167	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]	3/2017	337.75 -	337.75	-	06/2019 -	06/2019
168	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]	2/2017	5,070.13 -	5,070.13	240.02	04/2020 -	04/2020
169	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]	2/2017	204.12 -	204.12	7.45	09/2019 -	09/2019
170	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]	3/2017	379.95 -	379.95	19.67	12/2019 -	12/2019
171	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]	2/2017	235.53 -	235.53	7.29	06/2019 -	06/2019
172	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODHISHA - [N18000243]	3/2017	162.31 -	162.31	.62	03/2019 -	03/2019
173	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]	2/2017	322.30 -	322.30	15.11	02/2019 -	02/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(October 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
174	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]	2/2017	195.05 -	195.05	-	02/2020 -	02/2020
175	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]	10/2016	608.24 -	608.24	6.28	04/2019 -	04/2019
176	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]	10/2016	408.46 -	408.46	41.84	01/2019 -	01/2019
177	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]	3/2017	283.72 -	283.72	7.71	11/2019 -	11/2019
178	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION - [N18000237]	10/2016	167.75 -	167.75	1.16	04/2019 -	04/2019
179	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]	3/2017	251.60 -	251.60	-	06/2019 -	06/2019
180	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]	11/2016	330.00 -	330.00	185.90	11/2017 -	11/2017
181	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]	9/2016	562.25 -	562.25	18.56	03/2019 -	03/2019
182	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232]	8/2016	177.52 -	177.52	10.95	02/2019 -	02/2019
183	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]	8/2016	431.89 -	431.89	.62	02/2019 -	02/2019
184	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]	7/2016	333.17 -	333.17	148.98	03/2019 -	03/2019
185	WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]	7/2016	150.99 -	150.99	29.37	07/2018 -	07/2018
186	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]	7/2016	300.94 -	300.94	32.90	12/2018 -	12/2018
187	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]	7/2016	1,429.38 -	1,429.38	113.56	01/2019 -	01/2019
188	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]	5/2016	167.01 -	167.01	40.22	11/2018 -	11/2018
189	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]	4/2016	844.64 -	844.64	126.12	04/2019 -	04/2019
190	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]	4/2016	790.13 -	790.30	289.21	06/2019 -	06/2019
191	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]	4/2016	287.99 -	287.99	75.18	06/2018 -	06/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(October 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
192	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I - [N18000220]	4/2016	810.48 -	810.48	355.87	12/2018 -	12/2018
193	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]	5/2016	14,733.37 -	14,733.37	698.45	11/2019 -	11/2019
194	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]	5/2016	3,519.59 -	3,519.59	446.63	05/2019 -	05/2019
195	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]	5/2016	766.21 -	766.21	59.23	11/2018 -	11/2018
196	NORTH EASTERN REGION STRENGTHENING SCHEME IV - [N18000216]	5/2016	409.19 -	409.19	55.00	05/2018 -	05/2018
197	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]	4/2016	454.11 -	454.11	81.02	04/2018 -	04/2018
198	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	1/2016	10,598.98 -	10,598.98	1,043.00	07/2020 -	07/2020
199	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,179.96	5,990.92	12/2009 03/2018	03/2018
200	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]	7/2015	2,247.37 -	2,247.37	688.65	07/2018 -	07/2018
201	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]	4/2015	1,479.30 -	1,479.30	726.01	04/2017 03/2018	03/2018
202	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]	5/2015	780.33 -	780.33	32.82	10/2018 -	10/2018
203	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]	3/2015	1,394.52 -	1,394.52	24.47	05/2017 06/2019	06/2019
204	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]	3/2015	197.40 -	197.40	48.84	03/2018 -	03/2018
205	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]	7/2010	1,272.80 -	1,731.10	1,417.01	11/2012 12/2017	12/2017
206	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP - [N18000180]	1/2015	268.80 -	340.88	161.96	03/2018 -	03/2018
207	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]	12/2014	6,517.36 -	6,517.36	3,477.53	04/2018 -	04/2018
208	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]	1/2016	207.88 -	207.88	90.85	07/2018 -	07/2018
209	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]	1/2016	1,455.47 -	1,455.47	557.91	07/2018 -	07/2018
210	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	9,870.51	3,537.00	09/2019 -	09/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(October 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
211	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	7/1998	368.72 -	1,329.43	1,288.82	07/2006 11/2017	11/2017
212	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	5/2005	1,779.29 -	2,187.32	1,958.79	11/2008 09/2018	09/2018
213	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]	12/2011	1,746.65 -	2,228.71	1,963.69	08/2014 12/2017	12/2017
214	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	426.29	361.27	08/2014 12/2017	12/2017
215	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,337.76	1,508.72	08/2013 03/2018	03/2018
216	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]	4/2010	4,404.57 -	5,135.01	3,464.70	01/2015 03/2018	03/2018
	Total		1,18,356.48 -	1,29,713.37	53,993.64		
	<u>RAILWAYS</u>						
217	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,750.00 -	1,295.42	19.80	03/2022 -	03/2022
218	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]	12/2015	1,762.94 -	1,762.94	-	12/2020 -	12/2020
219	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	4/2015	524.00 668.00	668.00	-	03/2020 -	03/2020
220	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE [N22000350]	12/2015	1,491.47 -	1,491.47	-	12/2020 -	12/2020
221	KIUL - GAYA DOUBLING PROJECT - [N22000349]	12/2015	1,200.20 -	1,200.20	-	12/2020 -	12/2020
222	JAGADALPUR-KORAPUT DOUBLING - [N22000376]	4/2015	1,547.38 -	1,547.38	34.69	03/2021 -	03/2021
223	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	169.16	03/2021 -	03/2021
224	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]	4/2016	5,200.00 -	5,200.00	-	03/2020 -	03/2020
225	RAMNA - SINGRAULI DOUBLING - [N22000417]	8/2015	2,436.21 -	2,436.21	79.66	03/2020 -	03/2020
226	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	8/2016	582.13 -	582.13	-	03/2020 -	03/2020
227	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	6/2016	2,478.23 -	2,478.23	-	03/2022 -	03/2022
228	BINA - KOTA DOUBLING WITH RE - [N22000414]	4/2011	1,485.65 -	1,485.85	686.19	12/2020 -	12/2020
229	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	3/2012	1,183.25 -	1,183.30	729.14	12/2020 -	12/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(October 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
230	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	3/2009	942.95 -	942.95	.16	03/2019 -	03/2019
231	RAIPUR - TITLAGARH - DOUBLING - [N22000411]	3/2007	758.09 -	758.09	826.51	03/2020 -	03/2020
232	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	3/2006	960.18 -	960.18	609.51	03/2020 -	03/2020
233	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	3/2009	1,514.45 -	1,514.45	-	03/2020 -	03/2020
234	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78 -	723.78	.22	12/2025 -	12/2025
235	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	4/2011	4,295.30 -	1,621.60	217.35	12/2026 -	12/2026
236	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]	4/2015	1,765.90 -	1,765.90	32.39	12/2025 -	12/2025
237	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	4/2011	927.01 -	977.00	739.55	03/2019 -	03/2019
238	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	728.10 -	728.10	25.08	12/2024 -	12/2024
239	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	4/2015	750.55 -	750.56	20.42	12/2024 -	12/2024
240	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	4/1995	524.43 -	939.00	183.99	12/2021 -	12/2021
241	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	1/1991	763.18 -	1,428.00	482.05	12/2021 -	12/2021
242	BONDAMUNDA RANCHI DOUBLING - [N22000396]	3/2016	1,724.20 -	1,724.20	126.44	03/2021 -	03/2021
243	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	969.83	82.00	03/2020 -	03/2020
244	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	8/2016	234.50 -	234.50	.39	03/2019 -	03/2019
245	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]	10/2013	343.00 -	343.00	240.72	03/2019 -	03/2019
246	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]	12/2015	174.00 -	174.00	94.20	03/2019 -	03/2019
247	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]	12/2015	346.32 -	300.00	206.47	03/2019 -	03/2019
248	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]	5/2014	207.00 -	207.00	142.00	03/2018 -	03/2018
249	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]	1/2013	387.70 -	387.70	351.28	03/2018 -	03/2018
250	MULTI MODAL LOGISTICS PARK AT SWARUPGANJ - [N22000423]	4/2012	471.82 -	471.82	19.91	03/2019 -	03/2019
251	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]	10/2013	305.00 -	305.00	218.41	03/2019 -	03/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(October 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
252	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]	1/2011	493.17 -	493.17	383.12	03/2018 -	03/2018
253	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	9/2016	1,273.00 1,908.00	1,908.00	-	12/2021 -	12/2021
254	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	4/2015	701.61 -	701.61	37.66	03/2021 -	03/2021
	Total		44,562.91 -	43,296.95	6,758.47		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
255	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]	5/2015	454.89 -	454.89	22.74	05/2018 -	05/2018
256	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]	6/2016	829.00 -	829.00	59.85	01/2019 -	01/2019
257	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]	6/2015	463.49 -	463.49	9.26	06/2018 -	06/2018
258	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]	6/2015	437.39 -	437.39	21.86	06/2018 -	06/2018
259	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]	3/2015	168.39 -	168.39	16.84	11/2018 -	11/2018
260	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]	3/2015	194.11 -	194.11	30.54	05/2018 -	05/2018
261	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]	7/2015	197.16 -	197.16	38.50	10/2018 -	10/2018
262	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]	6/2015	774.57 -	774.57	-	03/2018 -	03/2018
263	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]	1/1991	218.63 -	218.63	29.27	10/2017 -	10/2017
264	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]	1/1991	219.40 -	219.40	-	01/2018 -	01/2018
265	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS [N24000357]	9/2015	567.51 -	567.51	-	03/2018 -	03/2018
266	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA-BARWALA - PANCHKULA(PKG - 2) [N24000358]	10/2015	562.34 -	562.34	292.94	04/2018 -	04/2018
267	JAISALMER - BARMER - [N24000348]	8/2015	482.27 -	482.27	-	02/2018 -	02/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(October 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
268	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349	5/2015	1,387.11 -	1,387.11	682.41	11/2017 -	11/2017
269	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347	8/2015	723.54 -	723.54	562.23	02/2018 -	02/2018
270	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337	8/2015	538.08 -	538.08	-	02/2018 -	02/2018
271	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463	12/2015	1,083.00 -	1,083.00	139.98	06/2018 -	06/2018
272	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450	9/2015	785.78 -	785.78	631.26	03/2018 -	03/2018
273	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448	1/2016	574.28 -	574.28	204.29	07/2018 -	07/2018
274	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446	9/2015	788.51 -	788.51	341.55	03/2018 -	03/2018
275	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445	8/2014	822.90 -	822.90	-	04/2018 -	04/2018
276	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440	9/2015	789.31 -	789.31	603.92	03/2018 -	03/2018
277	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438	12/2015	289.99 -	289.99	-	12/2018 -	12/2018
278	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436	9/2015	664.53 -	664.53	390.38	03/2018 -	03/2018
279	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433	9/2015	768.56 -	768.56	530.45	03/2018 -	03/2018
280	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657	3/2017	1,030.44 -	1,065.51	-	03/2020 -	03/2020
281	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	3/2017	744.64 -	982.00	-	03/2020 -	03/2020
282	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655	3/2017	247.02 -	157.49	-	03/2020 -	03/2020
283	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	3/2017	1,184.71 -	1,310.00	-	03/2020 -	03/2020
284	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653	3/2017	1,373.28 -	1,373.28	-	03/2020 -	03/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(October 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
285	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM [N24000589	6/2016	649.00 -	649.00	-	06/2019 -	06/2019
286	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587	6/2016	763.23 -	763.23	-	06/2019 -	06/2019
287	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586	6/2016	637.18 -	637.18	-	06/2019 -	06/2019
288	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499	12/2015	667.00 -	667.00	178.32	06/2018 -	06/2018
289	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	3/2017	993.16 -	1,434.00	-	03/2020 -	03/2020
290	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	3/2017	831.58 -	1,177.00	-	03/2020 -	03/2020
291	SIX LANING AND STRENGTHENING OF KM 340+000 TO KM 403+400 OF HUBLI-HAVERI SECTION OF NH-48 (OLD NH-4) - [N24000673	3/2017	985.41 -	1,200.00	-	03/2020 -	03/2020
292	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	3/2017	2,064.99 -	2,447.00	-	03/2020 -	03/2020
293	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	3/2017	1,288.07 -	1,420.00	-	03/2020 -	03/2020
294	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670	3/2017	239.68 -	235.90	-	03/2020 -	03/2020
295	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669	3/2017	165.50 -	172.16	-	03/2020 -	03/2020
296	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	3/2017	1,041.62 -	1,187.10	-	03/2020 -	03/2020
297	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667	3/2017	648.32 -	503.10	-	03/2020 -	03/2020
298	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666	3/2017	235.48 -	227.77	-	03/2020 -	03/2020
299	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	3/2017	672.89 -	736.01	-	03/2020 -	03/2020
300	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664	3/2017	639.79 -	552.90	12.08	03/2020 -	03/2020
301	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663	3/2017	1,989.00 -	1,989.00	-	03/2020 -	03/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(October 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
302	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	3/2017	754.54 -	756.27	-	03/2020 -	03/2020
303	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	3/2017	1,098.06 -	1,160.64	-	03/2020 -	03/2020
304	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	3/2017	988.34 -	1,043.28	-	03/2020 -	03/2020
305	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703	10/2017	964.17 -	964.17	-	10/2017 -	10/2017
306	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702	10/2017	639.97 -	639.97	-	10/2017 -	10/2017
307	JUNAGADH BYPASS - [N24000701	10/2017	232.49 -	232.49	-	10/2017 -	10/2017
308	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695	4/2017	388.00 -	447.37	-	10/2017 -	10/2017
309	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693	6/2017	1,958.88 -	1,958.88	-	06/2020 -	06/2020
310	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692	6/2017	2,485.93 -	2,485.93	-	06/2020 -	06/2020
311	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691	4/2017	894.00 -	894.00	-	04/2020 -	04/2020
312	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493	1/2016	1,027.53 -	1,027.53	163.91	06/2018 -	06/2018
313	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491	1/2016	815.28 -	815.28	99.71	06/2018 -	06/2018
314	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488	12/2015	2,136.97 -	2,136.97	-	12/2018 -	12/2018
315	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484	12/2015	239.23 -	239.23	168.16	12/2017 -	12/2017
316	FOUR LANING OF PARWANOO -SOLAN - [N24000479	9/2015	934.46 -	934.46	177.09	03/2018 -	03/2018
317	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478	12/2015	927.54 -	927.54	29.17	06/2018 -	06/2018
318	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475	11/2015	628.45 -	628.45	20.74	03/2018 -	03/2018
319	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471	12/2015	2,168.66 -	2,168.66	-	06/2019 -	06/2019
320	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651	2/2017	904.16 -	904.16	-	02/2020 -	02/2020
321	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642	3/2015	226.31 226.00	226.00	-	10/2017 -	10/2017

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(October 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
322	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641	2/2015	239.91 240.00	240.00	-	10/2017 -	10/2017
323	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640	1/2015	326.63 327.00	327.00	-	04/2018 -	04/2018
324	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523	12/2011	159.39 -	159.39	-	11/2017 -	11/2017
325	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508	7/2015	1,871.34 -	1,871.34	2,709.38	01/2018 -	01/2018
326	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500	1/2016	830.36 -	830.36	-	07/2018 -	07/2018
327	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430	12/2015	223.30 -	223.30	-	06/2018 -	06/2018
328	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429	12/2015	225.02 -	159.20	-	12/2018 -	12/2018
329	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421	3/2015	235.08 -	235.08	47.81	05/2018 -	05/2018
330	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414	1/1991	229.41 -	229.41	6.65	05/2018 -	05/2018
331	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411	11/2014	218.31 -	218.31	-	02/2018 -	02/2018
332	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410	6/2015	641.02 -	641.02	89.88	12/2017 -	12/2017
333	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409	5/2011	176.22 -	176.22	-	02/2018 -	02/2018
334	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397	1/1991	322.00 -	322.00	56.41	03/2018 -	03/2018
335	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	1/2014	267.16 352.00	352.05	.02	11/2017 -	11/2017
336	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333	12/2015	621.43 -	621.43	-	06/2018 -	06/2018
337	2 LANING WITH PAVED SHOULDER OF AGARTALA- UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328	10/2014	369.00 -	369.00	36.90	03/2018 -	03/2018
338	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327	3/2015	394.00 -	394.00	-	06/2018 -	06/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(October 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
339	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325	10/2015	179.82 -	179.82	8.99	01/2019 -	01/2019
340	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323	10/2014	588.95 -	588.95	80.00	11/2018 -	11/2018
	Total		62,408.05 -	64,400.53	8,493.49		
	<u>SHIPPING AND PORTS</u>						
341	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	2/2015	244.50 258.00	258.33	.14	12/2017 -	12/2017
342	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED [N25000068	9/2015	210.00 -	210.00	-	01/2018 -	01/2018
	Total		454.50 -	468.33	.14		
	<u>STEEL</u>						
343	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110	12/2007	200.00 -	200.00	131.15	03/2018 -	03/2018
344	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112	4/2013	170.00 -	170.00	88.91	04/2018 -	04/2018
345	ALTERNATE GAS NETWORK AT BSL - [N12000093	3/2015	255.19 -	255.19	168.02	03/2018 -	03/2018
346	NMDC INTEGRATED STEEL PLANT - [N12000086	1/2010	15,525.00 -	15,525.00	12,854.06	05/2015 10/2018	10/2018
347	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120	7/2015	465.85 -	465.85	41.38	07/2018 -	07/2018
348	CENTRAL DISPATCH YARD - [N12000119	8/2015	320.66 -	320.66	17.71	08/2018 -	08/2018
349	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115	11/2015	818.00 -	818.00	28.13	06/2020 -	06/2020
350	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118	11/2016	262.87 -	262.87	37.19	06/2019 -	06/2019
351	FORGED WHEEL PLANT - [N12000116	4/2014	1,682.85 -	1,682.85	63.22	09/2018 -	09/2018
	Total		19,700.42 -	19,700.42	13,429.77		
	<u>TELECOMMUNICATIONS</u>						
352	MAHARASHTRA NODAL (LOT 1) - [N26000107	8/2017	156.00 -	156.00	-	04/2018 -	04/2018
353	MADHYA PRADESH ACCESS (LOT1) - [N26000110	8/2017	215.30 -	215.30	-	05/2018 -	05/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(October 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
354	GUJARAT ACCESS (LOT 1) - [N26000111]	9/2017	171.54 -	171.54	-	04/2018 -	04/2018
355	MAHARASHTRA CORE (LOT1) - [N26000108]	8/2017	156.77 -	156.77	-	04/2018 -	04/2018
356	MAHARASHTRA ACCESS (LOT 1) - [N26000109]	8/2017	213.00 -	213.00	-	05/2018 -	05/2018
	Total		912.61 -	912.61	.00		
	<u>URBAN DEVELOPMENT</u>						
357	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]	2/2014	388.00 -	388.00	289.64	05/2017 02/2018	02/2018
358	RESIDENTIAL QUARTERS FOR HAL,BANGLORE - [N28000103]	12/2016	246.31 -	246.31	-	02/2020 -	02/2020
359	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB [N28000102]	8/2016	294.00 -	294.00	43.83	04/2019 -	04/2019
360	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL [N28000059]	12/2012	188.87 -	188.87	166.54	12/2015 12/2017	12/2017
361	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]	1/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 -	03/2019
362	CONSTRUCTION OF 1003 NOS 900 NOS TYPE 2 AND 54 NOS TYPE3 AND 33 NOS TYPE 4 AND 16 NOS TYPE 5 FAMILY - [N28000095]	12/2016	164.00 -	164.00	69.24	01/2018 05/2018	05/2018
363	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]	10/2016	209.84 -	209.84	.46	03/2020 -	03/2020
364	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]	6/2016	3,770.00 -	3,770.00	-	03/2018 -	03/2018
365	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN - [N28000091]	8/2014	350.02 -	479.87	388.94	03/2015 12/2017	12/2017
366	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,118.00	2,841.57	11/2019 -	11/2019
	Total		16,803.04 -	16,786.89	6,336.99		
	Grand Total		5,15,709.82	5,27,504.80	1,47,843.82		

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Annexure - XIII

Costing Rs.150 Crore and above					(October 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,000.00	09/2010 -	02/2018	71.82
	Total		3,492.00 -	6,000.00			
	<u>CIVIL AVIATION</u>						
2	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT [N04000050]	01/2009	309.46 -	553.53	01/2011 -	10/2017	78.87
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28
	Total		624.07 -	994.86			
	<u>COAL</u>						
4	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 -	486.57	03/2012 -	03/2018	87.58
5	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86
6	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80	11/2021 -	11/2021	.00
	Total		17,915.37 -	18,213.99			
	<u>DEFENCE PRODUCTION</u>						
7	CONSTRUCTION WORKS PHASE 4 - [N39000001]	12/2016	167.69 168.00	172.99	05/2018 -	05/2018	2.97
8	CONSTRUCTION WORKS PHASE 3B - [N39000002]	12/2016	285.95 286.00	296.05	08/2020 -	08/2020	3.51
	Total		453.64 -	469.04			
	<u>FERTILISERS</u>						
9	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. [N08000010]	02/2016	482.85 -	494.00	12/2017 -	12/2017	2.31
	Total		482.85 -	494.00			

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above (October 2017)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>HEALTH AND FAMILY WELFARE</u>						
10	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005]	11/2013	196.70 -	209.00	01/2016 -	-	6.25
	Total		196.70 -	209.00			
	<u>HEAVY INDUSTRY</u>						
11	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78
	Total		1,718.00 -	3,827.30			
	<u>PETROLEUM</u>						
12	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	439.03	03/2017 -	11/2018	24.53
13	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	11/2017	70.49
14	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	05/2013	4,124.35 -	5,637.00	04/2016 -	12/2017	36.68
15	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	03/2018	29.42
16	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	11/2017	37.72
17	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]	11/2011	310.00 -	370.00	03/2013 -	-	19.35
18	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	04/2018 -	04/2018	1.77
19	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]	05/2015	224.00 207.00	207.25	04/2019 -	04/2019	.12
	Total		12,125.58 -	15,459.12			
	<u>POWER</u>						
20	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	8,398.75	09/2009 -	12/2018	114.28
21	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	18,559.49	09/2010 -	-	195.28
22	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203]	02/2015	302.49 302.00	302.49	02/2016 -	-	.16

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(October 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
23	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	03/2020	29.14
24	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID [N18000169]	08/2014	288.49 -	376.09	02/2017 -	03/2018	30.37
25	SYSTEM STRENGTHENING XII OF SR - [N18000085]	02/2010	232.34 -	245.00	06/2012 -	12/2017	5.45
26	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	13,731.26	01/2018 -	12/2018	5.91
27	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT [N18000194]	05/2015	436.68 -	602.44	12/2016 -	12/2017	37.96
28	BOKARO THERMAL POWER STATION-A - [N18000199]	08/2006	2,313.00 4,139.00	4,366.64	12/2011 -	02/2017	5.50
29	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]	04/2007	4,122.00 8,781.00	9,142.58	02/2011 -	03/2016	4.12
30	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	3,939.11	02/2016 -	12/2020	137.73
31	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	426.29	08/2014 -	12/2017	43.37
32	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,882.01	01/2016 -	02/2018	61.50
33	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI-LEH PROJECT - [N18000215]	01/2014	1,788.41 -	2,333.71	09/2017 -	09/2018	30.49
34	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]	04/2016	790.13 -	790.30	06/2019 -	06/2019	.02
35	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]	03/2015	955.00 -	1,364.00	12/2015 -	03/2018	42.83
	Total		42,972.91 -	74,306.46			
	<u>RAILWAYS</u>						
36	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]	04/1986	158.77 274.56	634.48	03/1994 -	-	131.09
37	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	36.80 274.41	614.00	- -	-	123.75
38	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37	- -	-	141.40
39	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 -	920.00	- -	-	491.45
40	KATI HAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	492.98 -	1,320.00	12/2010 -	-	167.76
41	GULBARGA-BIDAR,SCR(NL) - [220100254]	02/1998	242.42 369.70	1,542.41	- 05/2009	-	317.21

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(October 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
42	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) [220100263]	03/1998	280.00 -	1,122.00 -	- -	-	300.71
43	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 -	2,125.18 -	- -	03/2021	543.99
44	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92 -	12/2006 -	-	224.37
45	GADWAL - RAICHUR (NL), SCR - [220100270]	04/1998	92.63 -	350.00 -	02/2011 -	-	277.85
46	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,319.33 -	- 12/2009	03/2019	10.97
47	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 -	973.33 -	12/2012 12/2012	-	60.33
48	JIND-SONEPAT (NL),NR - [220100280]	01/2004	238.56 -	740.00 -	03/2012 -	-	210.19
49	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	301.64 -	1,185.64 -	- 09/2009	03/2019	293.06
50	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	470.92 727.13	2,713.09 -	- -	03/2021	273.12
51	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	04/2003	218.19 -	412.05 -	- -	03/2018	88.85
52	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	142.45 -	228.40 -	- -	-	60.34
53	ETAWAH-MAINPURI (NL),NCR - [220100318]	04/1997	120.00 -	245.39 -	12/2008 -	-	104.49
54	HATHUA-BHATNI (N L) (NER) - [220100319]	04/2005	230.03 -	718.54 -	- -	05/2019	212.37
55	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	1,101.16 -	- -	-	186.92
56	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23 -	1,202.70 -	02/2015 -	12/2019	556.39
57	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	340.00 -	03/2009 03/2009	12/2017	64.25
58	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07 -	- -	12/2022	137.80
59	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]	04/2003	136.62 -	376.00 -	12/2007 03/2010	-	175.22
60	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1997	261.70 -	388.00 -	02/2006 -	12/2019	48.26
61	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	950.00 -	03/2010 -	03/2018	38.24
62	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU PONDY-AGASTIYAMPALLI [N22000079]	09/2007	404.19 -	2,072.50 -	- -	-	412.75
63	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	1,065.00 -	- -	-	210.34

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(October 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
64	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	2,300.00	-	-	404.39
65	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	-	60.77
66	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	4,600.00	04/2014 -	03/2020	642.73
67	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	332.92 283.95	477.88	03/2012 -	-	68.30
68	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56 -	1,160.47	- -	03/2022	206.55
69	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 -	1,825.00	03/2008 06/2008	03/2020	145.63
70	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	941.04	03/2014 -	06/2019	44.07
71	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,030.29	03/2012 -	-	70.85
72	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]	04/2006	117.36 196.95	203.00	03/2011 -	-	3.07
73	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	509.00	12/2012 -	05/2016	123.34
74	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	499.30 -	3,168.29	- -	03/2023	534.55
75	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 -	365.67	- -	-	.14
76	HANSDIHA-GODDA NL - [N22000236]	04/2011	267.09 -	350.78	- -	-	31.33
77	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	493.96 -	681.68	- -	-	38.00
78	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	04/2010	423.66 -	720.59	03/2017 -	-	70.09
79	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 -	199.12	- -	-	8.18
80	PEN ROHA DOUBLING - [N22000254]	04/2007	98.74 -	381.39	- -	-	286.26
81	PANVEL PEN DOUBLING - [N22000255]	04/2006	96.16 -	280.00	- -	-	191.18
82	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26
83	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	-	651.97
84	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,054.35 -	2,200.00	- -	-	108.66

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above (October 2017)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
85	GUDUR-DURGARAJAPATNAM - [N22000265]	04/2011	283.54 -	759.41	- -	-	167.83
86	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	197.17	- -	-	25.87
87	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	625.00	- -	-	117.77
88	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	4,500.00	- -	-	329.85
89	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	-	57.65
90	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	- -	-	47.93
91	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,714.49	- -	-	76.69
92	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29
93	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	792.01	- -	-	134.68
94	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63	- -	-	57.68
95	CHANDIGARH-BADDI NL - [N22000296]	04/2007	328.14 -	1,540.00	- -	-	369.31
96	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	-	14.14
97	MONIGRAM- NIMTITA - [N22000301]	04/2012	250.93 -	259.23	- -	-	3.31
98	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	04/2012	255.64 -	272.20	- -	-	6.48
99	JAGGAYYAPET - MELLACHERUVU - [N22000304]	04/2007	313.24 -	554.70	01/1999 -	-	77.08
100	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	750.00	01/1999 -	-	60.78
101	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	01/1999 -	-	53.96
102	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	514.68 -	2,271.50	- -	-	341.34
103	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]	04/1995	900.05 -	1,125.89	12/2011 12/2010	03/2020	25.09
104	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	09/1997	1,500.00 -	5,450.00	04/2008 12/2011	06/2018	263.33
105	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35
106	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	04/1997	501.69 335.77	1,043.56	03/2012 -	-	210.80
107	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	12/2009 -	-	300.67

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(October 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
108	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	541.00	- -	-	232.17
109	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	3,040.00	12/2008 -	03/2019	314.73
110	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	470.21 -	3,004.90	- -	06/2021	539.05
111	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	9,658.00	03/2011 -	03/2020	1,227.45
112	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	322.95 -	341.41	03/2012 -	-	5.72
113	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 -	732.89	06/2013 -	03/2018	47.84
114	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	465.00	03/2011 -	10/2011	173.53
115	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	780.00	- -	03/2019	290.00
116	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	300.00 -	2,135.00	- -	03/2020	611.67
117	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	850.00 -	3,000.00	03/2015 -	03/2020	252.94
118	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
119	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) [N22000119]	04/1999	207.52 -	334.87	12/2012 -	-	61.37
120	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT [N22000127]	04/1996	1,676.31 -	7,300.00	03/2009 -	03/2018	335.48
121	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	3,451.00	03/2014 -	03/2020	324.30
122	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	360.00	- -	-	27.24
123	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,084.69	12/2015 -	03/2020	204.95
124	KANPUR KASGANJ MATHURA(GC) NER - [220100197]	03/1997	677.97 1,062.36	1,679.13	- -	-	58.06
125	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]	04/1999	744.71 -	1,126.79	- -	-	51.31
126	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	780.98	- -	08/2018	90.45
127	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) [N22000114]	04/2008	516.23 -	735.00	03/2014 -	-	42.38
128	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above (October 2017)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
129	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	27,946.00	11/2002 -	12/2018	1,017.84
130	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	625.30 408.76	876.10	06/2007 -	-	114.33
131	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	04/2006	325.00 -	1,581.53	03/2010 -	-	386.62
132	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	1,195.00	12/2012 -	-	293.09
133	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	380.00	02/2009 02/2009	06/2017	128.70
134	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075	09/2006	324.90 -	516.40	03/2010 -	12/2017	58.94
135	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110	04/2010	3,951.98 -	4,259.48	03/2016 -	12/2020	7.78
136	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109	04/2010	2,298.42 -	2,733.86	03/2014 -	-	18.95
137	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192	03/1996	155.74 164.36	966.98	02/2009 -	12/2017	488.33
138	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	525.00	- -	03/2019	122.07
139	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	07/2008 -	-	284.00
140	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,776.81	03/1998 -	12/2019	359.96
141	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	-	564.94
142	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097	03/1984	293.97 -	749.69	06/2005 -	-	155.02
143	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	491.33	06/2004 -	-	153.17
144	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	- -	-	840.53
145	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345	04/1997	836.26 -	1,072.52	- -	-	28.25
146	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107	04/2007	482.00 -	874.57	03/2013 -	-	81.45
147	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123	04/2008	318.24 -	321.62	03/2012 -	03/2019	1.06
148	SAMBALPUR-TALCHER DOUBLING - [N22000315	03/2011	679.27 -	1,579.27	- -	03/2021	132.50
149	JHARSUGUDA-RENGALI DOUBLING - [N22000317	03/2006	201.00 -	230.00	- -	-	14.43

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(October 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
150	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	826.57 -	1,160.83	-	03/2020	40.44
151	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 -	238.03	-	03/2020	52.77
152	DELANG-PURI DOUBLING - [N22000320]	03/2011	165.16 -	234.71	03/2015 -	-	42.11
153	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	-	-	8.10
154	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]	04/2011	190.10 -	350.00	-	03/2019	84.11
155	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	209.00	12/2016 -	-	40.49
156	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	648.00	-	03/2020	8.00
157	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]	04/2008	829.74 -	1,161.64	03/2015 -	12/2019	40.00
158	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43 -	1,010.00	-	-	711.70
159	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	663.01 175.30	858.97	06/1999 -	-	390.00
160	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00 -	2,815.62	-	01/2018	411.93
161	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 -	308.00	-	-	.33
162	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 -	268.78	-	08/2017	10.26
163	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]	03/2008	195.64 -	474.30	-	03/2018	142.44
164	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	-	10/2018	61.80
165	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 -	644.00	-	-	.16
166	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	348.55	-	03/2019	41.64
167	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	567.18 -	975.62	-	03/2020	72.01
168	DHASA-JETALSAR (GC) - [N22000141]	04/2012	376.59 -	644.38	-	12/2020	71.11
169	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]	04/2011	439.88 -	845.68	-	-	92.25
170	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	399.63	-	03/2019	24.63
171	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	04/2013	1,266.89 -	1,548.66	-	12/2020	22.24

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(October 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
172	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	1,037.15	- -	03/2019	132.54
173	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]	04/2010	279.40 -	355.00	- -	-	27.06
174	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	2,562.27	- -	-	23.02
175	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	12/2022	226.98
176	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	276.89	- -	10/2018	16.87
177	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR [N22000152]	04/2013	456.00 -	855.16	- -	05/2018	87.54
178	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	-	17.92
179	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	272.99	- -	03/2019	27.93
180	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]	04/2012	288.97 -	369.08	- -	10/2018	27.72
181	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	293.68	- -	03/2019	21.31
182	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	12/2022	226.23
183	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00	- -	-	62.32
184	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00	- -	-	82.25
185	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
186	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	-	53.44
187	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]	04/2010	171.02 -	250.00	06/2013 -	12/2016	46.18
188	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	-	88.40
189	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	12/2017	41.36
190	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 -	549.75	- -	-	32.26
191	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
192	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
193	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	- -	-	338.91

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(October 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
194	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]	04/2008	678.62 -	2,393.23	- -	-	252.66
195	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
196	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	2,350.00	- -	-	348.88
197	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
198	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]	04/1998	271.24 -	520.00	- -	-	91.71
199	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,810.00	- -	03/2018	120.09
200	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
201	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	380.00	- -	-	71.62
202	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,857.00	03/2007 -	04/2016	107.49
203	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00 -	580.00	- -	07/2019	130.16
204	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77 -	630.00	- -	03/2018	200.33
205	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	450.00	- -	03/2019	58.70
206	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22	- -	-	109.04
207	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	302.90	- -	-	84.23
208	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	342.85	- -	-	78.83
209	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02 -	6,000.00	- -	03/2021	46.95
210	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00	- -	-	94.45
211	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	-	63.25
212	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	450.00	- -	03/2020	171.38
213	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	04/1999	523.17 -	1,871.00	- -	03/2018	257.63
214	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12 -	535.00	- -	03/2019	71.41
215	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	398.93	- -	03/2019	62.12

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above (October 2017)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
216	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2018	29.06
217	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	1,500.00	- -	-	149.41
218	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 -	260.60	- -	-	51.49
219	PIRPAINTI-BHAGALPUR - [N22000222]	04/2011	261.38 -	332.14	- -	-	27.07
220	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	02/2015	4,670.00 3,627.00	3,627.47	- -	-	.01
221	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	- -	-	10.94
222	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]	02/2016	854.00 -	1,035.16	- -	-	21.21
223	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.67	- -	-	9.32
224	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	559.91	07/2014 -	-	68.57
225	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS - [N22000386]	04/2003	4,300.00 -	4,520.00	- -	08/2015	5.12
226	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 -	871.00	- -	03/2021	.00
227	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) [N22000390]	04/2016	556.31 -	612.00	- -	-	10.01
228	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	01/1991	763.18 -	1,428.00	12/2021 -	12/2021	87.11
229	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	04/1995	524.43 -	939.00	12/2021 -	12/2021	79.05
230	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]	02/2015	900.00 -	4,131.90	- -	-	359.10
231	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	750.55 -	750.56	12/2024 -	12/2024	.00
232	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 -	2,373.00	03/2003 -	-	130.97
233	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	977.00	03/2019 -	03/2019	5.39
234	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	03/2012	1,183.25 -	1,183.30	12/2020 -	12/2020	.00
235	BINA - KOTA DOUBLING WITH RE - [N22000414]	04/2011	1,485.65 -	1,485.85	12/2020 -	12/2020	.01
	Total		1,18,068.43 -	2,83,702.40			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(October 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
236	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	12/2017	28.93
237	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	12/2017	92.75
238	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	03/2018	80.68
239	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	12/2017	68.99
240	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	03/2018	106.50
241	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]	01/2014	361.30 -	207.40	07/2014 -	-	-42.60
242	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	04/2010 -	03/2018	42.25
243	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	-	2.29
244	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]	03/2010	1,509.10 -	3,237.87	09/2012 -	12/2017	114.56
245	INDORE-JHABUA-GUJRAT/MP - [N24000136]	10/2010	1,175.00 -	1,206.10	04/2013 -	09/2017	2.65
246	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]	10/2014	295.47 -	313.27	02/2017 -	02/2017	6.02
247	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]	03/2011	218.31 -	339.82	12/2015 -	-	55.66
248	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	01/2014	255.75 348.00	348.43	09/2017 -	09/2017	.12
249	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]	01/2014	267.16 352.00	352.05	11/2017 -	11/2017	.01
250	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]	12/2014	201.12 201.00	201.12	02/2015 -	-	.06
251	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]	12/2009	104.00 -	201.00	09/2010 -	09/2010	93.27
252	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	05/2013	1,055.00 -	1,601.77	11/2015 -	09/2017	51.83
253	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	03/2017	1,184.71 -	1,310.00	03/2020 -	03/2020	10.58
254	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	03/2017	744.64 -	982.00	03/2020 -	03/2020	31.88
255	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	03/2017	1,030.44 -	1,065.51	03/2020 -	03/2020	3.40

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(October 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
256	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	03/2017	988.34 -	1,043.28	03/2020 -	03/2020	5.56
257	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]	03/2017	1,059.73 -	1,071.00	03/2017 -	-	1.06
258	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]	03/2017	1,098.06 -	1,160.64	03/2020 -	03/2020	5.70
259	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	03/2017	754.54 -	756.27	03/2020 -	03/2020	.23
260	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	03/2017	672.89 -	736.01	03/2020 -	03/2020	9.38
261	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]	03/2017	1,041.62 -	1,187.10	03/2020 -	03/2020	13.97
262	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]	03/2017	165.50 -	172.16	03/2020 -	03/2020	4.02
263	REHABILITATION AND UPGRADEATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]	03/2017	1,288.07 -	1,420.00	03/2020 -	-	10.24
264	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	03/2017	2,064.99 -	2,447.00	03/2020 -	03/2020	18.50
265	SIX LANING AND STRENGTHENING OF KM 340+000 TO KM 403+400 OF HUBLI-HAVERI SECTION OF NH-48 (OLD NH-4) - [N24000673]	03/2017	985.41 -	1,200.00	03/2020 -	03/2020	21.78
266	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]	03/2017	831.58 -	1,177.00	03/2020 -	03/2020	41.54
267	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]	03/2017	993.16 -	1,434.00	03/2020 -	03/2020	44.39
268	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]	04/2017	388.00 -	447.37	10/2017 -	10/2017	15.30
	Total		23,165.35 -	29,854.53			
	<u>SHIPPING AND PORTS</u>						
269	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	03/2006 -	12/2017	300.00
270	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065]	10/2013	198.94 -	235.15	06/2017 -	-	18.20
271	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]	02/2015	244.50 258.00	258.33	12/2017 -	12/2017	.13
272	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]	03/2007	245.67 -	409.83	04/2009 -	-	66.82

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(October 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
273	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72
	Total		1,205.50 -	2,172.77			
	<u>STEEL</u>						
274	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101	05/2005	768.88 1,070.97	1,113.34	02/2014 -	-	3.96
275	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	03/2018	42.39
276	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098	03/2007	149.73 173.00	175.94	12/2015 -	-	1.70
	Total		1,261.61 -	1,777.68			
	<u>TELECOMMUNICATIONS</u>						
277	NETWORK FOR SPECTRUM - [N26000101	03/2012	13,334.00 -	24,664.00	07/2015 -	06/2019	84.97
	Total		13,334.00 -	24,664.00			
	<u>URBAN DEVELOPMENT</u>						
278	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073	06/2010	205.00 -	170.62	03/2012 -	03/2018	-16.77
279	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100	02/2016	496.18 496.00	496.18	06/2017 -	-	.04
	Total		701.18 -	666.80			
	Grand Total		2,37,717.19	4,62,811.95			

List of Delayed Projects w.r.t. Latest Schedule

Annexure- XIV

Costing Rs.150 Crore and above						(October 2017)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI, TAMIL NADU	09/2003	3,492.00 5,677.00	6,000.00	5,499.43	09/2010 09/2016	02/2018	89	17
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 -	11,459.00	10,775.00	12/2015 11/2016	11/2019	47	36
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 -	12,320.00	8,399.00	12/2016 03/2017	12/2020	48	45
	Total		27,271.00 -	29,779.00	24,673.43				
	<u>CIVIL AVIATION</u>								
4	CONSTRUCTION OF NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT - [N04000050]AAI, SIKKIM	01/2009	309.46 -	553.53	522.95	01/2011 09/2017	10/2017	81	1
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	441.33	26.44	09/2018 -	06/2020	21	-
	Total		624.07 -	994.86	549.39				
	<u>COAL</u>								
6	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]NLC, TAMIL NADU	05/2016	687.28 830.45	830.45	705.43	06/2017 -	10/2017	4	-
7	RAJMAHAL OC EXP. - [N06000056]ECL, JHARKHAND	09/2009	153.82 -	153.82	127.71	03/2014 -	12/2017	45	-
8	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL, ODISHA	01/2005	302.96 -	302.96	329.10	03/2010 -	03/2018	96	-
9	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL, MADHYA PRADESH	10/2007	259.40 -	486.57	296.40	03/2012 -	03/2018	72	-
10	RKP OCP PHASE-I - [N06000079]SCCL, TELANGANA	03/2010	209.78 -	209.78	143.08	03/2015 -	03/2018	36	-
11	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL, TELANGANA	03/2010	181.19 -	181.19	159.87	03/2012 -	03/2018	72	-
12	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH	12/2009	321.50 -	321.50	198.95	03/2014 -	03/2018	48	-
13	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL, CHHATISGARH	11/2009	198.59 -	198.59	169.49	03/2016 -	03/2018	24	-
14	PURNADIH OCP (3.0 MTY) - [N06000085]JCL, JHARKHAND	07/2008	210.98 -	210.98	206.80	03/2013 -	03/2018	60	-
15	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]JCL, JHARKHAND	12/2009	510.85 -	510.85	341.12	03/2016 -	03/2018	24	-
16	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL, CHHATISGARH	04/2012	258.56 -	258.56	151.14	03/2016 -	03/2018	24	-
17	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL, TELANGANA	06/2012	365.01 -	365.01	83.80	06/2015 -	03/2018	33	-

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(October 2017)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
18	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 415.37	415.37	143.67	03/2016 -	03/2018	24	-
19	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	289.45	152.06	05/2014 -	04/2018	47	-
20	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	269.82	150.11	04/2014 -	04/2018	48	-
21	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.10 -	490.10	278.35	03/2017 -	05/2018	14	-
22	MURADIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	12.08	04/2014 -	10/2018	54	-
23	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	404.99	03/2013 -	11/2018	68	-
24	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 448.86	448.86	162.30	03/2012 -	03/2019	84	-
25	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	191.37	03/2010 -	03/2019	108	-
26	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	223.25	03/2012 -	03/2019	84	-
27	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	479.53	219.23	03/2013 -	03/2019	72	-
28	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	97.03	03/2012 -	03/2019	84	-
29	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	153.27	03/2012 -	03/2019	84	-
30	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	80.63	03/2014 -	03/2019	60	-
31	KOYAGUDEM OPENCASE PROJECT - [N06000146]SCCL,TELANGANA	10/2015	426.79 -	426.79	-	03/2018 -	03/2019	12	-
32	MOONIDH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	198.90	04/2015 -	04/2019	48	-
33	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	5.12	03/2014 -	03/2020	72	-
34	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	93.28	03/2011 -	03/2020	108	-
35	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 164.04	164.04	.34	03/2015 -	03/2020	60	-
36	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 349.28	349.28	1.31	03/2015 -	03/2020	60	-
37	KALYANIKHANI OPENCASE PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 417.33	417.33	59.26	07/2016 -	03/2020	44	-
38	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05 -	1,055.05	317.37	03/2018 -	03/2020	24	-
39	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	706.40 -	706.40	116.67	07/2012 03/2017	03/2021	104	48
40	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	437.51	259.34	03/2015 -	03/2021	72	-
41	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL,MULTI STATE	02/2017	328.00 -	328.00	45.31	03/2021 -	06/2022	15	-
42	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	489.62	48.58	03/2012 -	03/2023	132	-

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(October 2017)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
43	BHANEGAON OC - [N06000121]WCL,MAHARASHTRA	02/2015	187.94 409.68	409.68	72.23	03/2023 02/2017	03/2023	0	73
	Total		13,617.13 -	14,563.33	6,398.94				
	<u>STEEL</u>								
44	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND	10/2013	245.67 -	245.67	196.21	05/2016 -	11/2017	18	-
45	3RD CONVERTER AND 4TH CASTER - [N12000088]RINL,ANDHRA PRADESH	07/2011	974.76 -	974.76	586.93	07/2016 -	11/2017	16	-
46	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	18,052.70	03/2013 -	12/2017	57	-
47	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	227.00	199.95	12/2016 -	12/2017	12	-
48	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	488.40	227.98	10/2016 -	03/2018	17	-
49	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY- JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 253.92	253.92	193.97	06/2016 -	03/2018	21	-
50	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND	05/2015	1,154.18 -	1,154.18	477.34	12/2017 -	05/2018	5	-
51	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	1,034.01	194.21	10/2017 -	07/2018	9	-
52	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	189.00	-	03/2017 -	08/2018	17	-
53	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH	12/2011	2,858.00 -	2,500.00	621.35	12/2017 -	10/2018	10	-
54	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	151.33	7.15	09/2017 -	12/2018	15	-
55	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	787.29	285.30	12/2016 -	12/2018	24	-
56	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA	04/2015	3,127.30 -	3,127.30	1,380.44	04/2018 -	02/2019	10	-
57	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72	-
	Total		29,542.07 -	29,353.86	23,074.74				
	<u>PETROLEUM</u>								
58	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KARNATAKA	01/2006	993.00 -	1,693.00	1,544.61	01/2012 -	11/2017	70	-
59	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	1,200.00	958.50	03/2015 -	11/2017	32	-

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(October 2017)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
60	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU	03/2013	3,110.36 -	3,110.36	2,863.96	11/2015 -	12/2017	25	-
61	DHDS REVAMP FOR MEETING BS-IV DIESEL QUALITY - [N16000218]CPCL,TAMIL NADU	02/2016	367.11 -	367.11	225.34	04/2017 -	12/2017	8	-
62	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL,TAMIL NADU	05/2015	257.87 -	257.87	139.96	11/2016 -	02/2018	15	-
63	FUEL QUALITY UPGRADATION (DHDT/DHDS) PROJECT AT GUJARAT REFINERY - [N16000245]IOCL,GUJARAT	02/2016	931.00 -	931.00	400.75	07/2017 -	02/2018	7	-
64	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM	03/2009	228.64 -	209.19	147.06	12/2016 -	03/2018	15	-
65	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	439.03	126.43	03/2017 -	11/2018	20	-
66	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE	06/2009	2,915.00 -	2,915.00	1,269.70	12/2012 -	02/2019	74	-
67	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	10/2015	607.06 714.25	714.25	276.85	10/2017 -	03/2019	17	-
68	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	390.52 -	390.52	98.70	03/2019 -	04/2019	1	-
69	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]BPCL,MAHARASHTRA	02/2016	554.00 -	554.00	25.73	02/2020 -	01/2021	11	-
	Total		11,578.47 -	12,781.33	8,077.59				
	POWER								
70	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,552.00	4,552.00	2,229.09	10/2017 12/2016	10/2017	0	10
71	SYSTEM STRENGTHENING XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	245.00	238.62	06/2012 -	12/2017	66	-
72	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 2,702.65	2,702.65	2,338.48	09/2014 06/2017	12/2017	39	6
73	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 882.13	882.13	721.43	11/2014 06/2017	12/2017	37	6
74	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	01/2012	15,166.19 -	15,166.19	14,506.00	01/2017 07/2017	12/2017	11	5
75	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE	05/2014	829.98 -	829.98	410.67	08/2016 10/2017	12/2017	16	2
76	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 206.42	206.42	134.03	03/2016 07/2017	12/2017	21	5
77	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 225.28	225.28	133.69	02/2016 08/2017	12/2017	22	4

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(October 2017)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
78	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN,BIHAR	05/2015	436.68 -	602.44	473.75	12/2016 -	12/2017	12	-
79	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH	01/2016	305.04 -	305.04	161.56	03/2017 10/2017	12/2017	9	2
80	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	135.62	09/2014 09/2017	01/2018	40	4
81	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A) - [N18000254]PGCIL,MULTI STATE	04/2015	2,525.00 -	2,525.00	1,370.00	11/2017 -	01/2018	2	-
82	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,882.01	5,073.99	01/2016 -	02/2018	25	-
83	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 738.48	738.48	649.35	09/2010 12/2017	03/2018	90	3
84	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 8,149.00	8,149.00	6,815.00	09/2011 06/2017	03/2018	78	9
85	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 703.10	703.10	581.72	06/2015 12/2017	03/2018	33	3
86	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	2,011.63	12/2015 12/2017	03/2018	27	3
87	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 1,891.41	1,891.41	1,166.14	04/2016 09/2017	03/2018	23	6
88	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 550.18	550.18	366.29	11/2016 11/2017	03/2018	16	4
89	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE	08/2014	288.49 -	376.09	226.73	02/2017 06/2017	03/2018	13	9
90	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]PGCIL,MULTI STATE	03/2015	955.00 1,161.00	1,364.00	1,083.00	12/2015 -	03/2018	27	-
91	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24 -	1,071.24	465.53	09/2017 -	04/2018	7	-
92	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	5,151.37	1,622.82	03/2018 -	06/2018	3	-
93	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE	01/2015	871.62 -	871.62	146.64	10/2017 10/2017	06/2018	8	8
94	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN	07/2015	307.18 -	307.18	174.58	11/2017 -	06/2018	7	-
95	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE	04/2015	3,705.61 -	3,705.61	2,144.69	04/2018 -	07/2018	3	-

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(October 2017)			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
96	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 639.46	639.46	485.42	06/2014 03/2018	09/2018	51	6
97	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	03/2013	11,638.55 -	11,638.55	8,244.00	09/2017 03/2018	09/2018	12	6
98	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT - [N18000215]PGCIL,JAMMU AND KASHMIR	01/2014	1,788.41 -	2,333.71	1,204.26	09/2017 -	09/2018	12	-
99	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA	02/2014	12,532.44 -	12,532.44	6,433.00	08/2018 -	11/2018	3	-
100	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	8,398.75	6,529.67	09/2009 -	12/2018	111	-
101	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	8,128.00	11/2016 12/2017	12/2018	25	12
102	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	12/2012	11,846.00 -	11,846.00	8,673.00	06/2017 12/2017	12/2018	18	12
103	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 260.03	260.03	165.86	07/2017 -	12/2018	17	-
104	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 294.60	294.60	133.33	02/2014 02/2018	12/2018	58	10
105	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 -	13,731.26	10,084.21	01/2018 -	12/2018	11	-
106	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 7,998.00	7,998.00	6,838.73	05/2014 09/2017	02/2019	57	17
107	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	6,957.91	12/2016 -	02/2019	26	-
108	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 15,095.67	15,095.67	13,727.00	01/2011 05/2018	03/2019	98	10
109	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	808.63	207.14	01/2018 -	03/2019	14	-
110	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH	09/2014	9,188.98 -	9,188.98	3,231.00	03/2019 -	06/2019	3	-
111	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	4,754.42	399.63	12/2018 -	12/2019	12	-
112	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	5,111.33	363.42	12/2018 -	12/2019	12	-
113	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 -	3,846.30	3,321.00	03/2013 06/2019	03/2020	84	9
114	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 -	14,366.58	5,674.00	02/2019 02/2020	09/2020	19	7
115	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	2,491.58	1,264.31	06/2013 -	11/2020	89	-
116	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	3,939.11	2,394.81	02/2016 09/2019	12/2020	58	15

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(October 2017)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
117	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC, WEST BENGAL	09/2014	1,381.84 -	1,381.84	294.00	09/2019 -	03/2021	18	-
118	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL, JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	881.41	04/2020 12/2017	06/2023	38	66
	Total		1,92,327.99 -	2,19,632.36	1,41,016.16				
	<u>HEAVY INDUSTRY</u>								
119	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS, MULTI STATE	04/2011	1,718.00 -	3,827.30	2,289.00	09/2011 -	12/2017	75	-
	Total		1,718.00 -	3,827.30	2,289.00				
	<u>HEALTH AND FAMILY WELFARE</u>								
120	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC, WEST BENGAL	12/2014	168.90 -	168.90	108.00	05/2017 -	03/2018	10	-
121	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC, DELHI	12/2013	204.44 -	204.44	137.00	05/2017 -	06/2018	13	-
122	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC, PUNJAB	07/2016	152.95 -	152.95	34.00	02/2018 -	08/2018	6	-
123	AIIMS - OPD (NEW) - [N21000009]HSCC, DELHI	08/2014	293.65 -	293.65	207.00	05/2017 -	09/2018	16	-
	Total		819.94 -	819.94	486.00				
	<u>RAILWAYS</u>								
124	NANDYAL-YERRAGUNTALA (NL), SCR - [220100192]SCR, ANDHRA PRADESH	03/1996	155.74 164.36	966.98	874.72	02/2009 -	12/2017	106	-
125	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL, ODISHA	04/2000	133.41 207.00	340.00	-	03/2009 03/2009	12/2017	105	105
126	SALKA ROAD - ANUPNAGAR LINE DOUBLING - [N22000075]RVNL, CHHATISGARH	09/2006	324.90 -	516.40	710.67	03/2010 -	12/2017	93	-
127	UDHNA-JALGAON WITH ELECTRIFICATION (DOUBLING) (WR) - [N22000122]WR, GUJARAT	04/2008	1,389.62 -	1,389.62	1,513.78	03/2014 -	12/2017	45	-
128	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP, TAMIL NADU	04/2006	495.74 495.74	732.89	407.91	06/2013 -	03/2018	57	-
129	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, MADHYA PRADESH	09/2007	687.20 -	950.00	679.56	03/2010 -	03/2018	96	-
130	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR, ASSAM	04/1996	1,676.31 -	7,300.00	7,082.91	03/2009 -	03/2018	108	-
131	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR, ASSAM	09/1997	1,500.00 -	5,450.00	4,837.30	04/2008 12/2011	06/2018	122	78

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(October 2017)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
132	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	4,874.58	1,881.65	03/2016 -	06/2018	27	-
133	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 19,565.00	27,946.00	15,803.00	11/2002 -	12/2018	193	-
134	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	2,913.50	714.40	03/2016 -	12/2018	33	-
135	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL, TELANGANA	04/2012	632.68 -	816.55	461.84	03/2016 -	12/2018	33	-
136	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	733.00 -	3,040.00	2,389.60	12/2008 -	03/2019	123	-
137	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	1,319.33	757.23	- 12/2009	03/2019	-	111
138	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, ODISHA	04/1996	301.64 -	1,185.64	-	- 09/2009	03/2019	-	114
139	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 -	7,986.04	2,423.55	03/2014 -	03/2019	60	-
140	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR, GUJARAT	04/2008	318.24 -	321.62	37.15	03/2012 -	03/2019	84	-
141	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR, UTTAR PRADESH	08/2015	528.57 -	528.57	61.44	03/2018 -	03/2019	12	-
142	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113]NWR, RAJASTHAN	04/2008	653.19 -	941.04	653.42	03/2014 -	06/2019	63	-
143	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, MULTI STATE	02/1997	386.30 -	1,776.81	967.96	03/1998 -	12/2019	261	-
144	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA	04/1998	183.23 -	1,202.70	482.09	02/2015 -	12/2019	58	-
145	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]RVNL, JHARKHAND	03/1997	261.70 -	388.00	795.83	02/2006 -	12/2019	166	-
146	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR, RAJASTHAN	04/2008	829.74 -	1,161.64	456.30	03/2015 -	12/2019	57	-
147	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP, MAHARASHTRA	03/1996	495.44 1,781.98	1,781.98	667.06	03/2004 -	03/2020	192	-
148	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER, JHARKHAND	04/1995	900.05 -	1,125.89	980.99	12/2011 12/2010	03/2020	99	111
149	JIRIBAM TO IMPHAL (TUPII)(NL)(NEFR) - [220100288]NFR, MANIPUR	04/2003	727.56 -	9,658.00	5,464.91	03/2011 -	03/2020	108	-
150	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, ANDHRA PRADESH	07/2006	743.00 -	1,825.00	1,410.14	03/2008 06/2008	03/2020	144	141
151	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA	04/2008	813.34 -	3,451.00	2,365.89	03/2014 -	03/2020	72	-
152	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	619.34 -	4,600.00	1,749.95	04/2014 -	03/2020	71	-

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above (October 2017)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
153	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	4,084.69	383.92	12/2015 -	03/2020	51	-
154	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	385.60	27.69	03/2013 -	03/2020	84	-
155	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00 -	3,000.00	368.41	03/2015 -	03/2020	60	-
156	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA	03/2015	960.00 578.00	578.00	306.27	- 11/2015	03/2020	-	52
157	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	4,259.48	1,464.73	03/2016 -	12/2020	57	-
158	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 -	2,499.71	25.30	03/2021 -	03/2022	12	-
159	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 -	2,361.74	17.49	03/2021 -	03/2022	12	-
160	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 -	3,845.60	1.92	02/2020 -	12/2022	34	-
161	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANTPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 -	2,030.50	10.34	02/2019 -	12/2022	46	-
162	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	6,093.31	972.82	05/2008 -	03/2023	178	-
	Total		46,670.15 -	1,25,628.41	60,210.14				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
163	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	314.51	06/2008 -	10/2017	112	-
164	DEOLI KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	593.00	-	07/2013 -	10/2017	51	-
165	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	351.54	-	05/2013 -	10/2017	53	-
166	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	577.00	09/2013 -	10/2017	49	-
167	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	1,573.00	1,850.00	09/2015 -	10/2017	25	-
168	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH	03/2015	271.45 -	271.45	-	10/2015 -	10/2017	24	-
169	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	167.64	276.13	11/2008 -	11/2017	108	-
170	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	245.00	216.62	03/2008 -	11/2017	116	-
171	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	-	07/2013 -	11/2017	52	-
172	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	1,112.95	03/2013 -	11/2017	56	-

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above (October 2017)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
173	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	165.67	-	11/2015 -	11/2017	24	-
174	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	159.12	-	11/2015 -	11/2017	24	-
175	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	351.34	391.33	01/2016 -	11/2017	22	-
176	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	495.78	522.62	01/2016 -	11/2017	22	-
177	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	923.04	481.02	11/2016 -	11/2017	12	-
178	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	361.00	410.80	02/2009 -	12/2017	106	-
179	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	385.13	214.03	04/2009 -	12/2017	104	-
180	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	200.00	250.85	04/2009 -	12/2017	104	-
181	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	208.00	-	04/2008 -	12/2017	116	-
182	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	331.23	342.62	07/2009 -	12/2017	101	-
183	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	3,237.87	-	09/2012 -	12/2017	63	-
184	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	2,284.33	05/2013 -	12/2017	55	-
185	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	-	08/2012 -	12/2017	64	-
186	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	-	08/2014 -	12/2017	40	-
187	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	2,051.04	03/2013 -	12/2017	57	-
188	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,329.10	12/2013 -	12/2017	48	-
189	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	237.00	05/2013 -	12/2017	55	-
190	2 LANING OF DINDIGUL - PERIGULAM THENI-KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	406.68	08/2013 -	12/2017	52	-
191	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	622.89	10/2013 -	12/2017	50	-
192	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	-	11/2013 -	12/2017	49	-

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(October 2017)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
193	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	-	06/2014 -	12/2017	42	-
194	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,400.66	08/2013 -	12/2017	52	-
195	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI, ODISHA	12/2011	1,047.00 -	1,047.00	1,629.83	06/2014 -	12/2017	42	-
196	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	1,396.18	2,710.14	09/2014 -	12/2017	39	-
197	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH	07/2012	291.36 -	291.36	320.46	01/2014 -	12/2017	47	-
198	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI, UTTARAKHAND	11/2011	478.51 -	478.00	409.17	10/2013 -	12/2017	50	-
199	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI, JHARKHAND	12/2012	1,479.00 -	1,479.00	842.15	06/2015 -	12/2017	30	-
200	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI, MULTI STATE	10/2012	1,928.22 -	1,928.22	2,488.00	04/2015 -	12/2017	32	-
201	BARSAT-KRISHNANAGAR - [N24000229]NHAI, WEST BENGAL	08/2012	867.00 -	867.00	278.17	02/2015 -	12/2017	34	-
202	JALANDHAR - AMRITSAR - [N24000351]NHAI, PUNJAB	01/2014	523.85 -	523.85	250.08	01/2016 -	12/2017	23	-
203	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI, RAJASTHAN	02/2008	1,673.70 -	1,673.70	3,165.42	10/2011 -	12/2017	74	-
204	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI, CHHATISGARH	02/2013	1,232.00 -	1,232.00	-	08/2015 -	12/2017	28	-
205	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI, MAHARASHTRA	01/2015	972.50 -	972.50	1,460.25	07/2017 -	01/2018	6	-
206	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, ASSAM	12/2003	160.00 -	160.00	205.46	05/2008 -	02/2018	117	-
207	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI, HIMACHAL PRADESH	11/2013	1,916.79 -	1,916.79	1,884.41	11/2016 -	02/2018	15	-
208	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, ASSAM	12/2003	155.04 -	280.13	195.35	11/2008 -	03/2018	112	-
209	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, ASSAM	12/2003	217.61 -	309.56	389.87	04/2010 -	03/2018	95	-
210	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA	05/2009	1,108.00 -	2,288.00	3,882.53	11/2011 -	03/2018	76	-
211	JORBAT - BARAPANI - [N24000180]NHAI, MEGHALAYA	01/2011	536.00 -	536.00	-	01/2014 -	03/2018	50	-
212	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, BIHAR	01/2011	575.00 -	575.00	-	07/2013 -	03/2018	56	-
213	PANIKHOLI-RIMOLI - [N24000197]NHAI, ODISHA	03/2012	1,410.00 -	1,410.00	1,555.96	09/2014 -	03/2018	42	-
214	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL	02/2011	998.79 -	998.79	1,940.09	08/2013 -	03/2018	55	-
215	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL	02/2012	702.16 -	702.16	518.12	07/2014 -	03/2018	44	-
216	PANVEL-INDAPUR - [N24000216]NHAI, MAHARASHTRA	12/2011	942.69 -	942.69	373.84	06/2014 -	03/2018	45	-

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(October 2017)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
217	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	1,790.50	02/2014 -	03/2018	49	-
218	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	1,266.60	-	09/2016 -	03/2018	18	-
219	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	1,655.01	-	08/2016 -	03/2018	19	-
220	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	1,170.52	2,082.05	06/2012 -	03/2018	69	-
221	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	191.08	-	08/2015 -	03/2018	31	-
222	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	-	03/2014 -	04/2018	49	-
223	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	597.00	-	10/2017 -	04/2018	6	-
224	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	-	02/2013 -	06/2018	64	-
225	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	563.92	95.89	12/2017 -	06/2018	6	-
226	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 -	261.09	58.72	05/2017 -	06/2018	13	-
227	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU	11/2014	563.92 -	563.92	186.50	11/2016 -	06/2018	19	-
228	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	602.95	266.77	06/2016 -	06/2018	24	-
229	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	611.65	253.48	06/2016 -	06/2018	24	-
230	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	641.17	64.90	07/2016 -	07/2018	24	-
231	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA	06/2016	157.30 157.00	157.00	-	06/2018 -	11/2018	5	-
232	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	-	07/2015 -	03/2019	44	-
233	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	1,012.90	-	03/2016 -	03/2019	36	-
234	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 -	447.29	51.75	12/2017 -	04/2019	16	-

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(October 2017)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
235	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	373.07	-	08/2016 -	08/2019	36	-
236	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	396.52	-	08/2016 -	08/2019	36	-
237	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 -	429.52	-	08/2016 -	08/2019	36	-
238	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH	12/2016	138.93 155.00	155.00	-	01/2017 -	01/2020	36	-
	Total		62,070.98 -	65,613.60	45,642.04				
	<u>SHIPPING AND PORTS</u>								
239	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	600.00	139.80	03/2006 -	12/2017	141	-
240	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 -	669.46	411.12	12/2010 -	12/2018	96	-
	Total		516.39 -	1,269.46	550.92				
	<u>TELECOMMUNICATIONS</u>								
241	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	24,664.00	6,660.00	07/2015 -	06/2019	47	-
	Total		13,334.00 -	24,664.00	6,660.00				
	<u>URBAN DEVELOPMENT</u>								
242	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	332.72	260.88	09/2016 -	11/2017	14	-
243	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 19,058.00	19,058.00	14,784.59	12/2015 -	12/2017	24	-
244	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER - [N28000093]CPWD,KERALA	07/2015	154.00 -	154.00	71.90	11/2015 -	12/2017	25	-
245	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	119.37	08/2016 -	03/2018	19	-
246	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 349.33	349.33	252.50	03/2016 12/2017	03/2018	24	3

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(October 2017)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
247	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD, MAHARASHTRA	06/2010	205.00 166.97	170.62	146.41	03/2012 -	03/2018	72	-
248	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD, KERALA	01/2010	165.23 -	165.23	25.91	10/2012 04/2017	03/2018	65	11
249	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD, DELHI	07/2012	884.30 -	884.30	503.45	12/2015 12/2017	03/2018	27	3
250	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD, HIMACHAL PRADESH	11/2012	270.83 -	270.83	118.14	11/2014 -	10/2018	47	-
251	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD, MANIPUR	02/2014	216.69 -	216.69	52.00	03/2015 -	11/2018	44	-
252	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD, JHARKHAND	09/2012	171.86 -	171.86	38.63	03/2016 -	12/2018	33	-
253	NSG AT KOLKATA - [N28000104]CPWD, WEST BENGAL	10/2014	162.88 -	162.88	30.74	04/2018 -	06/2019	14	-
254	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD, UTTARAKHAND	12/2008	114.26 266.00	266.00	-	12/2013 -	10/2019	70	-
255	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL, KERALA	07/2012	5,181.79 -	5,181.79	-	07/2017 -	12/2019	29	-
256	NAGPUR METRO RAIL - [N28000085]NMRCL, MAHARASHTRA	08/2014	8,680.00 -	8,680.00	1,688.81	03/2018 -	12/2019	21	-
257	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL, KARNATAKA	02/2014	26,405.14 -	26,405.14	2,391.46	02/2019 -	03/2020	13	-
258	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD, DELHI	10/2013	1,219.21 2,230.23	1,592.00	136.13	10/2019 -	03/2020	5	-
	Total		59,161.81 -	64,217.96	20,620.92				
	Grand Total		4,59,252.00	5,93,145.41	3,40,249.27				

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(OCTOBER 2017)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12/2020	12320	48
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	11/2019	11459	47
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	02/2018	3492	89

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2020	314.61	21
5	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	AAI	01/2009	01/2011	10/2017	309.46	81

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
6	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY)	WCL	02/2017	03/2021	06/2022	328	15
7	RFR OF MANUGURU OC PROJECT	SCCL	11/2012	03/2016	03/2018	430.45	24
8	KALYANIKHANI OPENCAST PROJECT	SCCL	07/2012	07/2016	03/2020	417.33	44
9	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2020	162.76	60
10	JALAGAM VENGALA RAO OCP-II	SCCL	07/2011	03/2015	03/2021	447.06	72
11	BAROUD OC EXPANSION (RCE)- 3MTY	SECL	04/2012	03/2016	03/2018	258.56	24
12	RG OC -III EXTENSION (PHASE -II) PROJECT	SCCL	06/2012	06/2015	03/2018	365.01	33
13	KANIHA OCP, MCL, (10.0 MTY)	MCL	12/2007	03/2013	11/2018	457.77	68
14	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2009	03/2014	03/2018	321.5	48
15	BHUBANESWARI OCP, MCL (20.0 MTY)	MCL	12/2007	03/2017	05/2018	490.1	14
16	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	03/2012	03/2019	207.28	84
17	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2019	479.53	72
18	RKP OCP PHASE-I	SCCL	03/2010	03/2015	03/2018	209.78	36
19	BALRAM OCP EXTENSION, MCL 8.00 MTY	MCL	12/2007	03/2010	03/2019	172.08	108
20	MURAIIDIH UG TURN-KEY PROJECT	BCCL	02/2011	04/2014	10/2018	339.88	54

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(OCTOBER 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
21	MOONIDIH XV SEAM UG	BCCL	08/2011	04/2015	04/2019	1230.27	48
22	NORTH URIMARI OCP (3.0 MTY)	CCL	12/2007	03/2012	03/2019	179.87	84
23	TAPIN OCP (2.5 MTY)	CCL	08/2008	03/2012	03/2019	264.68	84
24	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2019	162.46	60
25	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2019	249.03	84
26	RAJMAHAL OC EXP.	ECL	09/2009	03/2014	12/2017	153.82	45
27	KISTARAM OCP	SCCL	11/2010	03/2015	03/2020	242.29	60
28	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2020	178.44	72
29	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	SECL	11/2009	03/2016	03/2018	198.59	24
30	MANUGURU OC-II EXTENSION PHASE-II	SCCL	03/2010	03/2012	03/2018	181.19	72
31	KOYAGUDEM OPENCAST PROJECT	SCCL	10/2015	03/2018	03/2019	426.79	12
32	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	60
33	MAGADH OC 20 MTY (CCL)	CCL	08/2008	07/2012	03/2021	706.4	104
34	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	03/2018	259.4	72
35	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2023	418.97	132
36	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2020	163.51	108
37	PURNADIH OCP (3.0 MTY)	CCL	07/2008	03/2013	03/2018	210.98	60
38	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	NLC	04/2013	06/2015	09/2019	1458.17	51
39	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	ECL	08/2012	03/2018	03/2020	1055.05	24
40	MADHUBAND NLW WASHERY	BCCL	08/2010	05/2014	04/2018	289.45	47
41	PATHERDIH NLW WASHERY	BCCL	10/2012	04/2014	04/2018	269.82	48
42	KULDA OCP (MAHANADI COALFIELDS LTD)	MCL	01/2005	03/2010	03/2018	302.96	96
43	RAJRAPPA RCE OCP (3.0 MTY)	CCL	12/2009	03/2016	03/2018	510.85	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(OCTOBER 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
44	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	04/2018	5907.11	28

FERTILISERS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
45	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	RCF	10/2014	11/2016	04/2019	197.79	29

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
46	NEIGRIHMS SHILLONG MEGHALYA	HSCC	10/2016	05/2018	08/2019	363.99	15
47	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	HSCC	07/2016	02/2018	08/2018	152.95	6
48	AIIMS - OPD(NEW)	HSCC	08/2014	05/2017	09/2018	293.65	16
49	AIIMS - MOTHER AND CHILD BLOCK	HSCC	12/2013	05/2017	06/2018	204.44	13
50	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	HSCC	12/2014	05/2017	03/2018	168.9	10

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
51	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	NATIS	04/2011	09/2011	12/2017	1718	75

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
52	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY	BPCL	02/2016	02/2020	01/2021	554	11
53	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	03/2018	309.81	41
54	TWENTY NOS. FEEDER GAS LINES	OIL	03/2009	12/2016	03/2018	228.64	15
55	PARADIP LPG IMPORT FACILITY	IOCL	01/2015	07/2018	06/2020	690	23
56	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY	CPCL	05/2015	11/2016	02/2018	257.87	15
57	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY	IOCL	03/2014	03/2017	10/2017	238.5	7
58	PIPELINE REPLACEMENT PROJECT -4	ONGC	02/2015	05/2017	05/2018	2899.93	12
59	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY	ONGC	08/2015	03/2019	05/2020	2818.88	14

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(OCTOBER 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
60	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	11/2019	202.94	70
61	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	12/2017	861.79	55
62	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	03/2018	2059.63	36
63	DEVELOPMENT OF C-26 CLUSTER FIELDS	ONGC	03/2012	05/2014	05/2018	2592.17	48
64	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD	ONGC	04/2012	12/2014	03/2018	600.17	39
65	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA	ONGC	01/2015	12/2017	03/2019	4619.94	15
66	SIX PIPELINE REPLACEMENT PROJECT	ONGC	03/2009	01/2017	03/2018	181.02	14
67	DHDS REVAMP FOR MEETING BS-IV DIESEL QUALITY	CPCL	02/2016	04/2017	12/2017	367.11	8
68	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	02/2019	2915	74
69	ASSAM RENEWAL PROJECT FOR GROUP A	ONGC	03/2009	03/2013	09/2018	2465.15	66
70	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	ONGC	06/2007	09/2011	06/2019	736.65	93
71	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	OIL	07/2011	03/2017	11/2018	352.56	20
72	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	11/2017	993	70
73	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	03/2019	607.06	17
74	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	12/2017	4124.35	20
75	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY	IOCL	03/2014	09/2017	06/2018	3076	9
76	POLYPROPYLENE PLANT AT PARADIP REFINERY	IOCL	03/2014	09/2017	12/2018	3150	15
77	RESID UPGRADATION PROJECT	CPCL	03/2013	11/2015	12/2017	3110.36	25
78	MH NORTH REDEVELOPMENT PHASE III	ONGC	06/2014	05/2017	05/2018	5706.47	12
79	PIPELINE REPLACEMENT PROJECT, AHMEDABAD	ONGC	09/2011	07/2016	06/2018	202.25	23
80	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	11/2017	871.35	32
81	SONAMURA GGS AND PIPELINE PROJECT (PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A	ONGC	05/2016	06/2017	01/2018	215.38	7
82	NEW 250 TMTA LPG PLANT AT PANAGARH	HPCL	08/2014	09/2017	03/2018	190.45	6

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(OCTOBER 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
83	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	05/2019	4588.29	9
84	FUEL QUALITY UPGRADATION (DHDT/DHDS) PROJECT AT GUJARAT REFINERY	IOCL	02/2016	07/2017	02/2018	931	7

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
85	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	12/2019	5111.33	12
86	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT	PGCIL	01/2014	09/2017	09/2018	1788.41	12
87	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	PGCIL	03/2016	01/2018	03/2019	808.63	14
88	EASTERN REGION STRENGTHENING SCHEME- III	PGCIL	07/2010	11/2012	12/2017	1272.8	61
89	INSTALLATION OF STATCOMS IN WESTERN REGION	PGCIL	03/2015	09/2017	04/2018	1071.24	7
90	SYSTEM STRENGTHENING XII OF SR	PGCIL	02/2010	06/2012	12/2017	232.34	66
91	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	PGCIL	03/2015	05/2017	06/2019	1394.52	25
92	DHUKWAN SMALL HYDRO PROJECT	THDCIL	05/2011	02/2014	12/2018	195.42	58
93	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	02/2019	5353	57
94	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	12/2016	12/2017	436.68	12
95	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A	PGCIL	04/2015	04/2017	03/2018	1479.3	11
96	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	12/2017	297.33	40
97	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	CVPPPL	10/2014	04/2020	06/2023	8112.12	38
98	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	02/2019	09/2020	14366.58	19
99	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	03/2021	1381.84	18
100	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP)	PGCIL	01/2015	10/2017	06/2018	871.62	8
101	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII	PGCIL	01/2015	07/2017	12/2018	203.28	17
102	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	12/2017	1746.65	40
103	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	02/2018	3642.04	25

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(OCTOBER 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
104	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	09/2018	1779.29	118
105	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	03/2019	8692.97	98
106	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	11/2017	368.72	136
107	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION	PGCIL	03/2012	09/2014	01/2018	198.63	40
108	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV	PGCIL	11/2011	11/2014	12/2017	723.63	37
109	KUDGI STPP STAGE 1	NTPC	01/2012	01/2017	12/2017	15166.19	11
110	EASTERN REGION STRENGTHENING SCHEME-XII	PGCIL	05/2014	11/2016	03/2018	522.29	16
111	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B	PGCIL	03/2014	03/2016	12/2017	155.57	21
112	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	03/2020	2978.48	84
113	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	03/2018	4375.35	78
114	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID	PGCIL	08/2014	02/2017	03/2018	288.49	13
115	EASTERN REGION STRENGTHENING SCHEME - IX	PGCIL	02/2014	02/2016	12/2017	196.58	22
116	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B	PGCIL	07/2015	11/2017	06/2018	307.18	7
117	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	11/2020	2491.58	89
118	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	03/2018	2496.9	99
119	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	PGCIL	09/2011	09/2014	12/2017	1940.13	39
120	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	12/2020	1657	58
121	SYTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	09/2018	487.49	51
122	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	03/2018	573.99	55
123	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A	PGCIL	03/2015	12/2015	03/2018	955	27
124	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	01/2018	12/2018	12964.6	11
125	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	12/2016	02/2019	9750.89	26
126	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2018	3919.59	111

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(OCTOBER 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
127	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	03/2018	477.69	90
128	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	02/2018	4824.12	64
129	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER	PGCIL	04/2010	01/2015	03/2018	4404.57	38
130	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	09/2017	09/2018	11638.55	12
131	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	12/2017	11130.19	52
132	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	02/2018	2144	62
133	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	03/2018	1364.52	23
134	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	PGCIL	01/2014	04/2016	12/2017	374.63	20
135	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX	PGCIL	02/2014	06/2016	02/2018	539.82	20
136	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII	PGCIL	02/2014	06/2016	11/2017	908.08	17
137	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION	PGCIL	05/2014	08/2016	12/2017	829.98	16
138	SOLAPUR STPP	NTPC	03/2012	11/2016	12/2018	9395.18	25
139	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	06/2017	12/2018	11846	18
140	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C	PGCIL	03/2013	06/2015	03/2018	514.2	33
141	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B	PGCIL	03/2013	12/2015	03/2018	2514.88	27
142	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW)	PGCIL	01/2016	03/2017	12/2017	305.04	9
143	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	12/2019	4754.42	12

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
144	KARAILA ROAD - SHAKTINAGAR DOUBLING	ECR	08/2015	03/2018	03/2019	528.57	12
145	KOTTAVALSA - KORAPUT DOUBLING	ECOR	04/2015	03/2021	03/2022	2499.71	12
146	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2018	2500	193
147	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	03/2010	12/2017	324.9	93
148	NEW WORK FOR CONSTRUCTION OF METRO	RVNL	04/2010	03/2016	12/2020	3951.98	57

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(OCTOBER 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
149	RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) NANDYAL-YERRAGUNTLA(NL),SCR	SCR	03/1996	02/2009	12/2017	155.74	106
150	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	03/1998	12/2019	386.3	261
151	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR)	WR	04/2008	03/2014	12/2017	1389.62	45
152	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	WR	04/2008	03/2012	03/2019	318.24	84
153	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2013	03/2020	394.14	84
154	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	NWR	04/2008	03/2015	12/2019	829.74	57
155	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	03/2018	687.2	96
156	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2020	619.34	71
157	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	03/2008	03/2020	743	144
158	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	12/2018	2913.51	33
159	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	NWR	04/2008	03/2014	06/2019	653.19	63
160	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	03/2020	495.44	192
161	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	ER	04/1995	12/2011	03/2020	900.05	99
162	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2018	1500	122
163	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2023	247.66	178
164	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	NFR	04/2000	12/2008	03/2019	733	123
165	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2020	727.56	108
166	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	03/2018	495.74	57
167	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2020	850	60
168	MUMBAI URBAN TRANSPORT PROJECT PHASE- II	M RTP	04/2008	03/2014	03/2019	5300	60
169	LUMDING-SILCHAR JIRIBAM, BADARPUR- BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	03/2018	1676.31	108
170	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2020	813.34	72

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(OCTOBER 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
171	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	51
172	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	12/2019	183.23	58
173	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	12/2017	133.41	105
174	GOELKERA-MANOHARPUR, (LD)(SER)	RVNL	03/1997	02/2006	12/2019	261.7	166
175	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	NCR	04/2010	02/2019	12/2022	622.41	46
176	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	M RTP	03/2013	03/2016	06/2018	4874.58	27
177	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	12/2022	1176.09	34
178	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2018	632.68	33
179	KORAPUT - SINGAPUR ROAD DOUBLING	ECOR	04/2015	03/2021	03/2022	2361.74	12

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
180	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	NHIDCL	03/2016	08/2016	08/2019	429.52	36
181	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTTEE KANON AND NAGPUR BYPASS	NHAI	04/2010	06/2012	03/2018	1170.52	69
182	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA	NHAI	06/2015	03/2016	03/2019	1012.9	36
183	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	08/2013	12/2017	1078.84	52
184	4-LANING OF BRAHAMPUR-FARAKA	NHAI	02/2011	08/2013	03/2018	998.79	55
185	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	NHAI	12/2011	06/2014	12/2017	1047	42
186	6-LANING OF DHANKUNI-KHARAGPUR SECTION	NHAI	04/2012	09/2014	12/2017	1396.18	39
187	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	NHAI	07/2012	01/2014	12/2017	291.36	47
188	ETAWAH CHAKERI	NHAI	03/2013	09/2015	10/2017	1573	25
189	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	12/2017	1928.22	32
190	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	NHAI	01/2015	07/2017	01/2018	972.5	6
191	4-LANING OF SOLAPUR - MAHARASHTRA/KARNATAKA SECTION	NHAI	06/2014	11/2016	11/2017	923.04	12
192	KRISHNANAGAR-BERHAMPUR	NHAI	02/2012	07/2014	03/2018	702.16	44

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(OCTOBER 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
193	RANCHI-RARGA-JAMSETHPUR	NHAI	12/2012	06/2015	12/2017	1479	30
194	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	03/2018	1108	76
195	DEOLI KOTA	NHAI	01/2011	07/2013	10/2017	593	51
196	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	NHAI	05/2013	02/2014	03/2018	1348.2	49
197	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM	NHAI	02/2010	08/2012	12/2017	617	64
198	PUNE-SATARA(NH-4)	NHAI	10/2010	03/2013	12/2017	1724.55	57
199	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM	NHAI	11/2010	05/2013	12/2017	1585	55
200	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM)	NHAI	11/2013	11/2016	02/2018	1916.79	15
201	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	NHAI	03/2016	07/2016	07/2018	641.17	24
202	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES	PWD	03/2015	10/2015	10/2017	271.45	24
203	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP	MORTH	03/2015	11/2015	11/2017	165.67	24
204	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU	MORTH	03/2015	11/2015	11/2017	159.12	24
205	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA	PWD	12/2011	08/2015	03/2018	191.08	31
206	BARSAT-KRISHNANAGAR	NHAI	08/2012	02/2015	12/2017	867	34
207	4 LANING OF NAGPUR-BETUL	NHAI	02/2011	08/2014	12/2017	2498.76	40
208	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	NHAI	07/2010	07/2015	03/2019	1987	44
209	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	NHAI	07/2010	07/2013	11/2017	1813.76	52
210	PATNA-MUZZAFFARPUR	NHAI	08/2010	02/2013	06/2018	671.3	64
211	2 LANNING OF MOKAMA-MUNGER	NHAI	05/2011	05/2013	10/2017	351.54	53
212	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS	NHAI	05/2010	05/2013	12/2017	374	55
213	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI	NHAI	09/2011	08/2013	12/2017	485	52
214	JORBAT - BARAPANI	NHAI	01/2011	01/2014	03/2018	536	50
215	4-LANNING OF CHAPRA-HAJIPUR	NHAI	01/2011	07/2013	03/2018	575	56

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(OCTOBER 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
216	2 LANNING OF MUZAFFARPUR - SONBARSA	NHAI	05/2011	11/2013	12/2017	511.54	49
217	SRINAGAR TO BANIHAL	NHAI	06/2011	06/2014	12/2017	1100.7	42
218	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	03/2018	1266.6	18
219	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	NHAI	03/2010	09/2012	12/2017	1509.1	63
220	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	NHAI	09/2011	12/2013	12/2017	1250	48
221	TIRUPATI - TIRUTHANI - CHENNAI	NHAI	04/2011	10/2013	12/2017	571	50
222	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	04/2018	2848	49
223	PANIKHOLI-RIMOLI	NHAI	03/2012	09/2014	03/2018	1410	42
224	BAREILY-SITAPUR (NH-24)	NHAI	03/2011	09/2013	10/2017	1046	49
225	MUZAFFARNAGAR-HARIDWAR	NHAI	09/2011	03/2013	11/2017	754	56
226	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	NHAI	05/2014	08/2016	03/2018	1655.01	19
227	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	NHAI	02/2008	10/2011	12/2017	1673.7	74
228	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	NHAI	12/2003	05/2008	02/2018	160	117
229	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	12/2017	196	101
230	HARIDWAR DEHRADUN APPROVED LENGTH 69	NHAI	11/2011	10/2013	12/2017	478.51	50
231	PANVEL-INDAPUR	NHAI	12/2011	06/2014	03/2018	942.69	45
232	JALANDHAR - AMRITSAR	NHAI	01/2014	01/2016	12/2017	523.85	23
233	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	NHAI	06/2015	12/2017	06/2018	563.92	6
234	FOUR LANING OF VARANASI BYPASS	NHAI	05/2015	05/2017	06/2018	261.09	13
235	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232	NHAI	04/2014	01/2016	11/2017	351.34	22
236	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI	NHAI	04/2014	01/2016	11/2017	495.78	22
237	THANJAVUR - PUDUKOTTAI SECTION OF NH-226	NHAI	11/2014	11/2016	06/2018	563.92	19

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(OCTOBER 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
238	2 LANING WITH PS OF GULABPURA - UNIARA	NHAI	10/2015	10/2017	04/2018	597	6
239	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	NHAI	12/2015	06/2016	06/2018	602.95	24
240	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I)	NHAI	12/2015	06/2016	06/2018	611.65	24
241	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION	NHAI	02/2013	08/2015	12/2017	1232	28
242	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	NHAI	12/2003	02/2009	12/2017	280	106
243	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	12/2017	199.81	104
244	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	NHAI	12/2003	11/2008	11/2017	167.64	108
245	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	03/2018	155.04	112
246	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	NHAI	12/2003	04/2009	12/2017	200	104
247	SONAPUR TO GUWAHTI (AS-3)	NHAI	12/2003	03/2008	11/2017	245	116
248	BRAHMPUTRA BRIDGE, NH NO-31	NHAI	12/2003	04/2010	03/2018	217.61	95
249	NALBARI T BIJNI (AS-7)	NHAI	12/2003	04/2008	12/2017	208	116
250	NALBARI TO BIJNI (AS-6)	NHAI	12/2003	06/2008	10/2017	225	112
251	FOUR LANING OF CHANDIGARH - KHARAR	NHAI	10/2015	12/2017	04/2019	447.29	16
252	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	NHIDCL	12/2016	01/2017	01/2020	138.93	36
253	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	NHIDCL	03/2016	08/2016	08/2019	373.07	36
254	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	NHIDCL	03/2016	08/2016	08/2019	396.52	36

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
255	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT TR	01/2007	12/2010	12/2018	366.39	96
256	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	12/2017	150	141

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
257	COKE OVEN BATTERY-5	RINL	12/2011	12/2017	10/2018	2858	10

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(OCTOBER 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
258	NEW SINTER PLANT AT BOKARO STEEL PLANT	SAIL	03/2015	10/2017	07/2018	1034.01	9
259	INSTALLATION OF NEW HOT STRIP MILL AT RSP	SAIL	04/2015	04/2018	02/2019	3127.3	10
260	3RD CONVERTER AND 4TH CASTER	RINL	07/2011	07/2016	11/2017	974.76	16
261	REBUILDING OF COB-7 AT BSL	SAIL	10/2013	05/2016	11/2017	245.67	18
262	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	HSC	12/2007	12/2016	12/2017	202.61	12
263	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGALAYA UNDER NLCP	HSC	04/2014	09/2017	12/2018	151.33	15
264	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS	HSC	05/2015	03/2017	08/2018	189	17
265	IRRIGATION WORK OF BAGMATI	HSC	10/2005	03/2015	03/2021	956	72
266	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND	HSC	12/2007	06/2016	03/2018	253.92	21
267	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII	HSC	02/2014	12/2016	12/2018	787.29	24
268	EXPANSION OF BHILAI STEEL PLANT	SAIL	08/2010	03/2013	12/2017	17265	57
269	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	10/2018	15525	41
270	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	03/2018	343	17

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
271	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	06/2019	13334	47

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
272	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	10/2019	114.26	70
273	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	CPWD	07/2012	12/2015	03/2018	884.3	27
274	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA	CPWD	06/2010	03/2012	03/2018	205	72
275	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	CPWD	09/2012	03/2016	12/2018	171.86	33
276	CONSTRUCTION OF PERMANENT CAMPUS OF	CPWD	02/2014	08/2016	03/2018	156.57	19

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(OCTOBER 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	IISER KOLKATA AT HARINGHANTA KALYANI NADIA						
277	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN	CPWD	08/2014	03/2015	12/2017	350.02	33
278	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	CPWD	02/2014	03/2015	11/2018	216.69	44
279	NSG AT KOLKATA	CPWD	10/2014	04/2018	06/2019	162.88	14
280	BANGALORE METRO RAIL PROJECT PHASE-2	BMRCL	02/2014	02/2019	03/2020	26405.14	13
281	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	CPWD	02/2014	05/2017	02/2018	388	9
282	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL	CPWD	12/2012	12/2015	12/2017	188.87	24
283	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM	CPWD	04/2014	09/2016	11/2017	332.72	14
284	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	CPWD	11/2012	11/2014	10/2018	270.83	47
285	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	CPWD	02/2011	03/2016	03/2018	241.33	24
286	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	CPWD	01/2010	10/2012	03/2018	165.23	65
287	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	12/2017	14600	24
288	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	12/2019	5181.79	29
289	NAGPUR METRO RAIL	NMRCL	08/2014	03/2018	12/2019	8680	21
290	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AT IISER	CPWD	07/2015	11/2015	12/2017	154	25

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN RS. 100 CRORE

(OCTOBER 2017)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	6000	2508

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
2	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	AAI	01/2009	01/2011	309.46	553.53	244.07
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	314.61	441.33	126.72

COAL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
4	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	152.43	459.49	307.06
5	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	249.03	448.86	199.83
6	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	162.76	349.28	186.52
7	NEYVELI SOLAR POWER PROJECT 130 MW	NLC	05/2016	06/2017	687.28	830.45	143.17
8	BHANEGAON OC	WCL	02/2015	03/2023	187.94	409.68	221.74
9	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	259.4	486.57	227.17

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
10	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	NATIS	04/2011	09/2011	1718	3827.3	2109.3

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
11	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	993	1693	700
12	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	607.06	714.25	107.19
13	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	ONGC	12/2015	03/2023	658.62	910.23	251.61
14	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	871.35	1200	328.65
15	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	309.81	723.4	413.59
16	PARADIP HALDIA DURGAPUR LPG PIPELINE	IOCL	02/2011	06/2018	913	1330	417
17	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	2059.63	2665.65	606.02

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(OCTOBER 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
18	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	861.79	1256.72	394.93
19	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	202.94	330.35	127.41
20	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY	IOCL	03/2014	09/2017	3076	4190	1114
21	MH NORTH REDEVELOPMENT PHASE III	ONGC	06/2014	05/2017	5706.47	5813.25	106.78
22	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	4124.35	5637	1512.65
POWER							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
23	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	8398.75	4479.16
24	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	4824.12	5071.94	247.82
25	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	18559.49	12274.16
26	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	477.69	738.48	260.79
27	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	11130.19	13762.8	2632.61
28	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	3642.04	5882.01	2239.97
29	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	1746.65	2228.71	482.06
30	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	297.33	426.29	128.96
31	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	573.99	1337.76	763.77
32	SYTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	487.49	639.46	151.97
33	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	1657	3939.11	2282.11
34	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	PGCIL	09/2011	09/2014	1940.13	2702.65	762.52
35	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	2496.9	6179.96	3683.06
36	BOKARO THERMAL POWER STATION-A	DVC	08/2006	12/2011	2313	4366.64	2053.64
37	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A	PGCIL	03/2015	12/2015	955	1364	409
38	PAKRI BARWADIH COAL MINING PROJECT	NTPC	10/2004	10/2017	4237.96	4552	314.04

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(OCTOBER 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
39	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT	PGCIL	01/2014	09/2017	1788.41	2333.71	545.3
40	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C	PGCIL	03/2013	06/2015	514.2	703.1	188.9
41	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV	PGCIL	11/2011	11/2014	723.63	882.13	158.5
42	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	421.01	1078.31	657.3
43	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	368.72	1329.43	960.71
44	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	8692.97	15095.67	6402.7
45	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	1779.29	2187.32	408.03
46	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	12/2016	436.68	602.44	165.76
47	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	01/2018	12964.6	13731.26	766.66
48	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	5353	7998	2645
49	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	1272.8	1731.1	458.3
50	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	4375.35	8149	3773.65
51	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	3846.3	867.82
52	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	1364.52	1891.41	526.89
53	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	2144	2932.88	788.88
54	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	DVC	04/2007	02/2011	4122	9142.58	5020.58
55	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER	PGCIL	04/2010	01/2015	4404.57	5135.01	730.44
RAILWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
56	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	NCR	04/1986	03/1994	158.77	634.48	475.71
57	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR	NFR	04/1983	N.A.	36.8	614	577.2
58	CALICUT-MANGALORE (DL) (SR)	SR	02/1996	N.A.	240	579.37	339.37
59	KARUR-SALEM(NL), SR	SR	02/1997	N.A.	155.55	920	764.45
60	KATIHAR - JOGBANI (GC)(NEFR)	NFR	09/2001	12/2010	492.98	1320	827.02

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(OCTOBER 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
61	GULBARGA-BIDAR, SCR(NL)	SCR	02/1998	N.A.	242.42	1542.41	1299.99
62	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC)	SR	03/1998	N.A.	280	1122	842
63	RAICHUR-GUNTAKAL(DL)(SCR)	RVNL	04/2003	12/2007	136.62	376	239.38
64	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	N.A.	810.78	1928.07	1117.29
65	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	133.41	340	206.59
66	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	183.23	1202.7	1019.47
67	CHHINDWARA - NAGPUR (GC)(SECR)	SECR	04/2005	N.A.	383.79	1101.16	717.37
68	HATHUA-BHATNI (N L) (NER)	NER	04/2005	N.A.	230.03	718.54	488.51
69	ETAWAH-MAINPURI (NL),NCR	NCR	04/1997	12/2008	120	245.39	125.39
70	MAHARAJGANJ-MASRAKH (NL) - NER	NER	04/2003	N.A.	218.19	412.05	193.86
71	RAMGANJMUNDI-BHOPAL (NL),WCR	WCR	04/2001	N.A.	470.92	2713.09	2242.17
72	GUDUR-DURGARAJAPATNAM	SCR	04/2011	N.A.	283.54	759.41	475.87
73	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	N.A.	1054.35	2200	1145.65
74	BAGALKOT-KUDACHI NL	SWR	04/2010	N.A.	377.93	986.3	608.37
75	MUNIRABAD (GINGERA) -RAICHUR NL	SWR	04/2007	N.A.	179.65	1350.91	1171.26
76	TUMKUR-CHITRADURGA-DAVENGERE NL	SWR	04/2011	N.A.	913	1801.01	888.01
77	PANVEL PEN DOUBLING	CR	04/2006	N.A.	96.16	280	183.84
78	PEN ROHA DOUBLING	CR	04/2007	N.A.	98.74	381.39	282.65
79	WARDHA-SEWAGRAM NGP 3RD LINE	CR	04/2012	N.A.	297.85	540.02	242.17
80	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	N.A.	378.56	1160.47	781.91
81	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	1500	5450	3950
82	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	ER	04/1995	12/2011	900.05	1125.89	225.84

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(OCTOBER 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
83	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	495.44	1781.98	1286.54
84	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	N.A.	514.68	2271.5	1756.82
85	MM FROM PANSKURA-GHATAL NL	SER	04/2011	01/1999	276.69	426	149.31
86	MM FROM BURAMARA-CHAKULIA	SER	04/2008	01/1999	466.48	750	283.52
87	JAGGAYYAPET - MELLACHERUVU	SCR	04/2007	01/1999	313.24	554.7	241.46
88	GADAG-WADI NL	SWR	04/2013	N.A.	1117	1922	805
89	CHANDIGARH-BADDI NL	NR	04/2007	N.A.	328.14	1540	1211.86
90	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	4084.69	2745.21
91	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	813.34	3451	2637.66
92	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	1676.31	7300	5623.69
93	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	ER	04/1999	12/2012	207.52	334.87	127.35
94	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	5300	7986.04	2686.04
95	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	850	3000	2150
96	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	N.A.	300	2135	1835
97	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	N.A.	200	780	580
98	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	NFR	12/2006	03/2011	170	465	295
99	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	12/2021	1273	1908	635
100	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	1027.4	2373	1345.6
101	TRIVANDRUM-KANYAKUMARI DOUBLING	SR	02/2015	N.A.	900	4131.9	3231.9
102	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO	SER	04/1995	12/2021	524.43	939	414.57
103	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI	SER	01/1991	12/2021	763.18	1428	664.82
104	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS	NFR	04/2003	N.A.	4300	4520	220
105	MUZAFFARPUR-SITAMARHI NEW LINE	ECR	01/1991	07/2014	332.15	559.91	227.76

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(OCTOBER 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
106	MATHURA-PLWAL 4TH LINE (80KM)	NCR	04/2015	03/2020	524	668	144
107	VIJAYAWADA-GUDUR	RVNL	04/2015	N.A.	3246.26	3548.67	302.41
108	MANMAD - JALGAON - 3RD LINE (160 KM)	CR	02/2016	N.A.	854	1035.16	181.16
109	DAUND - MANMAD (236 KM)	CR	02/2016	N.A.	1876	2081.27	205.27
110	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	CR	02/2015	N.A.	2326	2449.91	123.91
111	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	CR	02/2015	N.A.	630	1272.19	642.19
112	PIRPAINTI-JASIDIH	ER	04/2013	N.A.	915.98	1130.13	214.15
113	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	N.A.	601.43	1500	898.57
114	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	632.68	816.55	183.87
115	LUMDING-HOJAI PATCH DOUBLING PROJECT	NFR	04/2012	N.A.	246.07	398.93	152.86
116	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	N.A.	312.12	535	222.88
117	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	NFR	04/1999	N.A.	523.17	1871	1347.83
118	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	N.A.	165.82	450	284.18
119	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	394.28	152.76
120	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	N.A.	242.22	471	228.78
121	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	N.A.	4083.02	6000	1916.98
122	CHENGANNUR-CHINGAVANAM	SR	04/2006	N.A.	191.72	342.85	151.13
123	MADURAI-BODINAYAKKANUR	SR	04/2008	N.A.	164.41	302.9	138.49
124	ERODE-PALANI	SR	04/2008	N.A.	288.57	603.22	314.65
125	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT	NFR	04/2012	N.A.	283.55	450	166.45
126	NEW COOCHBEHAR TO SAMUKTALA	NFR	04/2011	N.A.	209.77	630	420.23
127	AGARTALA-AKHAURA NL	NFR	04/2012	N.A.	252	580	328
128	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	03/2007	895	1857	962

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(OCTOBER 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
129	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	NFR	04/2010	N.A.	221.42	380	158.58
130	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	RVNL	04/2008	N.A.	822.39	1810	987.61
131	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	SR	04/1998	N.A.	271.24	520	248.76
132	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	SR	04/2013	N.A.	839	1500	661
133	CHENNAI-CUDDALORE VIA MAMALLAPURAM	SR	04/2008	N.A.	523.52	2350	1826.48
134	HAJIPUR-RAMDAYALUNAGAR DOUBLING	ECR	04/2013	N.A.	213.01	367.17	154.16
135	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)	ECR	04/2008	N.A.	678.62	2393.23	1714.61
136	MOTIHARI-SITAMARHI (NL)	ECR	04/2006	N.A.	211	926.09	715.09
137	SAKRI-HASANPUR ROAD (NL)	ECOR	04/1999	N.A.	175.69	325	149.31
138	GAYA-CHATRA (NL)	ECOR	04/2008	N.A.	415.67	549.75	134.08
139	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	N.A.	258.2	365	106.8
140	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	12/2015	309.44	583	273.56
141	BHADUTOLA-JHARGRAM VIA LALGARH (NL)	SER	04/2011	N.A.	289.64	760	470.36
142	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	N.A.	553.63	1009	455.37
143	BOWAICHANDI-ARAMBAGH	SER	04/2010	N.A.	267.37	434	166.63
144	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	NCR	04/2010	02/2019	622.41	2030.5	1408.09
145	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	NWR	04/2010	N.A.	739.65	872.22	132.57
146	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR	NWR	04/2013	N.A.	456	855.16	399.16
147	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	1176.09	3845.6	2669.51
148	RATLAM-DUNGARPUR VIA BANSWARA (NL)	NWR	04/2011	N.A.	2082.75	2562.27	479.52
149	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	N.A.	446	1037.15	591.15
150	PALANPUR-SAMAKHAYALI (DL)	RVNL	04/2013	N.A.	1266.89	1548.66	281.77
151	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC)	WR	04/2011	N.A.	439.88	845.68	405.8

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(OCTOBER 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
152	DHASA-JETALSAR (GC)	RVNL	04/2012	N.A.	376.59	644.38	267.79
153	AHMEDABAD-BOTAD (GC)	RVNL	04/2012	N.A.	567.18	975.62	408.44
154	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	N.A.	246.08	348.55	102.47
155	CHHAPRA-BALLIA UP	NER	03/2013	N.A.	295	477.31	182.31
156	BHOJIPUR TANAKPUR VIA PILIBHIT	NER	03/2008	N.A.	195.64	474.3	278.66
157	ANGAMALI-SABARIMALA (N.L.)(SR)	SR	10/1998	N.A.	550	2815.62	2265.62
158	AMRAVATI-NARKHER NL(CR)	CR	06/1994	06/1999	663.01	858.97	195.96
159	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	SCR	12/1994	N.A.	124.43	1010	885.57
160	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	NWR	04/2008	03/2015	829.74	1161.64	331.9
161	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	03/1998	386.3	1776.81	1390.51
162	MACHERLA-NALGONDA(NL)(SCR)	SCR	07/1998	07/2008	125	480	355
163	MUNEERABAD-MAHABOONNAGAR(NL), SCR	SCR	04/1997	N.A.	218.24	525	306.76
164	NANDYAL-YERRAGUNTALA(NL), SCR	SCR	03/1996	02/2009	155.74	966.98	811.24
165	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	2298.42	2733.86	435.44
166	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	3951.98	4259.48	307.5
167	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	03/2010	324.9	516.4	191.5
168	RAJATGARH-BARANG(LD), ECOR	RVNL	04/1999	02/2009	166.16	380	213.84
169	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL	RVNL	04/1995	12/2012	304	1195	891
170	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM)	RVNL	04/2011	N.A.	190.1	350	159.9
171	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	N.A.	826.57	1160.83	334.26
172	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	N.A.	679.27	1579.27	900
173	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	SWR	04/2007	03/2013	482	874.57	392.57
174	BANGLORE - SATYAMANGALAM (NL)(SWR)	SWR	04/1996	N.A.	138	1382.78	1244.78

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(OCTOBER 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
175	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM)	NER	04/1997	N.A.	836.26	1072.52	236.26
176	HUBLI-ANKOLA(NL),SWR	SWR	04/1997	N.A.	227	2135	1908
177	RANCHI-LOHARDAGA(GC),SER	SER	04/1997	06/2004	194.07	491.33	297.26
178	TAMLUK DIGHA,LINE DOUBLING (SER)	SER	03/1984	06/2005	293.97	749.69	455.72
179	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	393.46	1026	632.54
180	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	325	1581.53	1256.53
181	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	NR	03/2002	06/2007	625.3	876.1	250.8
182	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	NR	03/1995	11/2002	2500	27946	25446
183	NANGALDAM-TALWARA(NL),NR	NR	03/1981	07/2012	450	2100	1650
184	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR)	NWR	04/2008	03/2014	516.23	735	218.77
185	DAUSA-GANGAPUR CITY(NL),NWR	NWR	02/1997	N.A.	410.08	780.98	370.9
186	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	NER	04/1999	N.A.	744.71	1126.79	382.08
187	KANPUR KASGANJ MATHURA(GC) NER	NER	03/1997	N.A.	677.97	1679.13	1001.16
188	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	MRTTP	04/2006	06/2013	495.74	732.89	237.15
189	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	727.56	9658	8930.44
190	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	N.A.	470.21	3004.9	2534.69
191	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	NFR	04/2000	12/2008	733	3040	2307
192	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	541	378.13
193	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	12/2009	108	432.72	324.72
194	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	501.69	1043.56	541.87
195	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	6093.31	5845.65
196	HARIDWAR-LAKSAR	NR	04/2012	N.A.	219.83	346.63	126.8
197	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	N.A.	337.49	792.01	454.52

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(OCTOBER 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
198	RAYADURGA-TUMKUR NL	RVNL	04/2007	N.A.	970.34	1714.49	744.15
199	SHIMOGA-HARIHAR NL	SWR	04/2011	N.A.	562.74	832.47	269.73
200	SRINIVASA-PURA-MADANAPALLI NL	SWR	04/2013	N.A.	296	466.65	170.65
201	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	SWR	04/2013	N.A.	558	692.43	134.43
202	BHANUPALI-BILASPUR BERI NL	RVNL	04/2008	N.A.	1046.88	4500	3453.12
203	ROHTAK-MEHAM HANSI	NR	04/2012	N.A.	287	625	338
204	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	332.92	477.88	144.96
205	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	619.34	4600	3980.66
206	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	171.1	275.08	103.98
207	TIDIVANAM-NAGARI (NL)	SR	09/2006	N.A.	456	2300	1844
208	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	SR	09/2006	N.A.	343.17	1065	721.83
209	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI' -AGASTIYAMPALLI	SR	09/2007	N.A.	404.19	2072.5	1668.31
210	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	687.2	950	262.8
211	GOELKERA-MANOHARPUR, (LD)(SER)	RVNL	03/1997	02/2006	261.7	388	126.3
212	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC	ER	04/2010	03/2017	423.66	720.59	296.93
213	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	N.A.	493.96	681.68	187.72
214	KALYAN-KASARA 3RD LINE	CR	04/2011	N.A.	277.7	792.89	515.19
215	WARDHA-NANDED MAHARASHTRA	CR	04/2008	N.A.	499.3	3168.29	2668.99
216	KATAKHAL TO BHAIRABI	NFR	04/1998	12/2012	227.9	509	281.1
217	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2012	603.04	1030.29	427.25
218	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	NWR	04/2008	03/2014	653.19	941.04	287.85
219	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	03/2008	743	1825	1082
220	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	N.A.	330	2125.18	1795.18

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(OCTOBER 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
221	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	M RTP	03/2000	12/2006	1049.69	3404.92	2355.23
222	GADWAL - RAICHUR (NL), SCR	SCR	04/1998	02/2011	92.63	350	257.37
223	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	N.A.	1188.91	1319.33	130.42
224	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	12/2012	607.09	973.33	366.24
225	JIND-SONEPAT (NL),NR	NR	01/2004	03/2012	238.56	740	501.44
226	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	N.A.	301.64	1185.64	884
ROAD TRANSPORT AND HIGHWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
227	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	199.81	385.13	185.32
228	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O	NHAI	03/2017	03/2020	993.16	1434	440.84
229	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	NHAI	03/2017	03/2020	831.58	1177	345.42
230	SIX LANING AND STRENGTHENING OF KM 340+000 TO KM 403+400 OF HUBLI-HAVERI SECTION OF NH-48 (OLD NH-4)	NHAI	03/2017	03/2020	985.41	1200	214.59
231	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	NHAI	03/2017	03/2020	2064.99	2447	382.01
232	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	1288.07	1420	131.93
233	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	NHAI	03/2017	03/2020	1041.62	1187.1	145.48
234	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	NHAI	03/2017	03/2020	744.64	982	237.36
235	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	NHAI	03/2017	03/2020	1184.71	1310	125.29
236	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	11/2015	1055	1601.77	546.77
237	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S	PWD	03/2011	12/2015	218.31	339.82	121.51
238	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	NHAI	03/2010	09/2012	1509.1	3237.87	1728.77
239	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	PWD	12/2011	02/2012	156.63	276	119.37
240	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	1108	2288	1180
241	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	196	331.23	135.23
242	MAIBANG TO LUMDING (AS-24), KM.111.000	NHAI	12/2003	11/2008	155.04	280.13	125.09

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN RS. 100 CRORE

(OCTOBER 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
	TO KM.126.450						
SHIPPING AND PORTS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
243	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	150	600	450
244	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	03/2007	04/2009	245.67	409.83	164.16
245	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT	01/2007	12/2010	366.39	669.46	303.07
STEEL							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
246	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCL	05/2005	02/2014	768.88	1113.34	344.46
247	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	343	488.4	145.4
TELECOMMUNICATIONS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
248	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	13334	24664	11330
URBAN DEVELOPMENT							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
249	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	CPWD	02/2011	03/2016	241.33	349.33	108
250	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	1219.21	1592	372.79
251	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN	CPWD	08/2014	03/2015	350.02	479.87	129.85
252	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	114.26	266	151.74
253	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	14600	19058	4458

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(OCTOBER 2017)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	02/2018	3492.00	6000.00	2508	89

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2020	314.61	441.33	126.72	21
3	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	AAI	01/2009	01/2011	10/2017	309.46	553.53	244.07	81

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
4	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2020	162.76	349.28	186.52	60
5	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	03/2018	259.40	486.57	227.17	72
6	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2019	249.03	448.86	199.83	84
7	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	459.49	307.06	60

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
8	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	NATIS	04/2011	09/2011	12/2017	1718.00	3827.30	2109.3	75

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
9	UPGRADATION OF CRUDE OIL PUMP STATIONS OF MAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	11/2017	871.35	1200.00	328.65	32
10	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	03/2018	309.81	723.40	413.59	41
11	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	12/2017	861.79	1256.72	394.93	55
12	MH NORTH REDEVELOPMENT PHASE III	ONGC	06/2014	05/2017	05/2018	5706.47	5813.25	106.78	12

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(OCTOBER 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
13	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	12/2017	4124.35	5637.00	1512.65	20
14	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	11/2017	993.00	1693.00	700	70
15	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	03/2019	607.06	714.25	107.19	17
16	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY	IOCL	03/2014	09/2017	06/2018	3076.00	4190.00	1114	9
17	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	03/2018	2059.63	2665.65	606.02	36
18	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	11/2019	202.94	330.35	127.41	70

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
19	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR) - DRASS- KARGIL-KHALSTI-LEH PROJECT	PGCIL	01/2014	09/2017	09/2018	1788.41	2333.71	545.3	12
20	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV	PGCIL	11/2011	11/2014	12/2017	723.63	882.13	158.5	37
21	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	11/2017	368.72	1329.43	960.71	136
22	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	09/2018	1779.29	2187.32	408.03	118
23	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	12/2017	1746.65	2228.71	482.06	40
24	TRANSMISSION SYSTEM ASSOCIATED WITH IPSPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A	PGCIL	03/2015	12/2015	03/2018	955.00	1364.00	409	27
25	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	01/2018	12/2018	1,2964.60	1,3731.26	766.66	11
26	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2018	3919.59	8398.75	4479.16	111
27	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	02/2019	5353.00	7998.00	2645	57
28	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	12/2016	12/2017	436.68	602.44	165.76	12

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(OCTOBER 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
29	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	03/2018	2496.90	6179.96	3683.06	99
30	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	PGCIL	09/2011	09/2014	12/2017	1940.13	2702.65	762.52	39
31	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	12/2020	1657.00	3939.11	2282.11	58
32	SYTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	09/2018	487.49	639.46	151.97	51
33	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	03/2018	573.99	1337.76	763.77	55
34	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	12/2017	297.33	426.29	128.96	40
35	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	02/2018	3642.04	5882.01	2239.97	25
36	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	03/2018	477.69	738.48	260.79	90
37	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	02/2018	4824.12	5071.94	247.82	64
38	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER	PGCIL	04/2010	01/2015	03/2018	4404.57	5135.01	730.44	38
39	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	12/2017	1,1130.19	1,3762.80	2632.61	52
40	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	02/2018	2144.00	2932.88	788.88	62
41	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	03/2018	1364.52	1891.41	526.89	23
42	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	03/2020	2978.48	3846.30	867.82	84
43	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	03/2018	4375.35	8149.00	3773.65	78
44	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	12/2017	1272.80	1731.10	458.3	61
45	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	03/2019	8692.97	1,5095.67	6402.7	98
46	COMMON TR. SYS. ASSOCIATED	PGCIL	03/2013	06/2015	03/2018	514.20	703.10	188.9	33

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(OCTOBER 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C								

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
47	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2018	632.68	816.55	183.87	33
48	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	NCR	04/2010	02/2019	12/2022	622.41	2030.50	1408.09	46
49	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	03/1998	12/2019	386.30	1776.81	1390.51	261
50	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	03/2020	495.44	1781.98	1286.54	192
51	MANDARHILL -DUMKA-RAMPURHAT (NL), ER	ER	04/1995	12/2011	03/2020	900.05	1125.89	225.84	99
52	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2018	1500.00	5450.00	3950	122
53	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2023	247.66	6093.31	5845.65	178
54	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	03/2019	733.00	3040.00	2307	123
55	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2020	727.56	9658.00	8930.44	108
56	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	03/2018	495.74	732.89	237.15	57
57	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2020	850.00	3000.00	2150	60
58	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	03/2019	5300.00	7986.04	2686.04	60
59	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	03/2018	1676.31	7300.00	5623.69	108
60	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2020	813.34	3451.00	2637.66	72
61	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	4084.69	2745.21	51
62	UDHAMPUR-SRINAGAR-BARAMULLA	NR	03/1995	11/2002	12/2018	2500.00	2,7946.00	25446	193

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(OCTOBER 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	(NL), NR								
63	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	03/2010	12/2017	324.90	516.40	191.5	93
64	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	12/2020	3951.98	4259.48	307.5	57
65	NANDYAL-YERRAGUNTALA(NL), SCR	SCR	03/1996	02/2009	12/2017	155.74	966.98	811.24	106
66	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	12/2019	183.23	1202.70	1019.47	58
67	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	12/2017	133.41	340.00	206.59	105
68	GOELKERA-MANOHARPUR, (LD)(SER)	RVNL	03/1997	02/2006	12/2019	261.70	388.00	126.3	166
69	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	03/2018	687.20	950.00	262.8	96
70	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2020	619.34	4600.00	3980.66	71
71	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	03/2008	03/2020	743.00	1825.00	1082	144
72	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR)	NWR	04/2008	03/2014	06/2019	653.19	941.04	287.85	63
73	HIMMATNAGAR - UDAIPUR GAUGE CONVESSION (NWR)	NWR	04/2008	03/2015	12/2019	829.74	1161.64	331.9	57
74	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	12/2022	1176.09	3845.60	2669.51	34

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
75	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	12/2017	196.00	331.23	135.23	101
76	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	NHAI	03/2010	09/2012	12/2017	1509.10	3237.87	1728.77	63
77	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	03/2018	1108.00	2288.00	1180	76
78	MAIBANG TO LUMDING (AS-25),	NHAI	12/2003	04/2009	12/2017	199.81	385.13	185.32	104

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(OCTOBER 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	KM.83.400 TO KM.111.000								
79	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	03/2018	155.04	280.13	125.09	112

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
80	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT TRU	01/2007	12/2010	12/2018	366.39	669.46	303.07	96
81	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	12/2017	150.00	600.00	450	141

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
82	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	03/2018	343.00	488.40	145.4	17

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
83	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	06/2019	1,3334.00	2,4664.00	11330	47

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
84	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	10/2019	114.26	266.00	151.74	70
85	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN	CPWD	08/2014	03/2015	12/2017	350.02	479.87	129.85	33
86	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	12/2017	1,4600.00	1,9058.00	4458	24
87	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	CPWD	02/2011	03/2016	03/2018	241.33	349.33	108	24

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

Details of Ongoing Projects Under -Public Private Partnership Mode

Annexure- XVIII

Costing Rs.150 Crore and above					(October 2017)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>MINES</u>							
1	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT RAJASTHAN - PPP (ANNUITY) - [N10000009]	12/2015	344.50 -	344.50	11/2016 -	11/2016	.00	0
	Total		344.50 -	344.50				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
2	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - PPP (BOT) - [N24000208]	07/2012	291.36 -	291.36	01/2014 -	12/2017	.00	47
3	INDORE-DEWAS(NH-3) - PPP (BOT) - [N24000159]	11/2010	325.00 -	325.00	05/2013 -	07/2017	.00	50
4	2 LANNING OF MOKAMA-MUNGER - PPP (ANNUITY) - [N24000166]	05/2011	351.54 -	351.54	05/2013 -	10/2017	.00	53
5	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - PPP (ANNUITY) - [N24000176]	05/2010	374.00 -	374.00	05/2013 -	12/2017	.00	55
6	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - PPP (ANNUITY) - [N24000177]	09/2011	485.00 -	485.00	08/2013 -	12/2017	.00	52
7	DELHI/ HARYANA BORDER TO ROHTAK - PPP (BOT) - [N24000122]	04/2007	486.00 -	486.00	05/2010 -	08/2017	.00	87
8	2 LANNING OF MUZAFFARPUR - SONBARSA - PPP (ANNUITY) - [N24000188]	05/2011	511.54 -	511.54	11/2013 -	12/2017	.00	49
9	TRICHY - KARUR - PPP (BOT) - [N24000528]	03/2007	516.00 -	516.00	07/2008 -	-	.00	0
10	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - PPP (BOT) - [N24000426]	11/2012	530.07 -	530.07	08/2016 -	-	.00	0
11	JORBAT - BARAPANI - PPP (ANNUITY) - [N24000180]	01/2011	536.00 -	536.00	01/2014 -	03/2018	.00	50
12	TALEGAON-AMRAVATI - PPP (BOT) - [N24000140]	11/2009	567.00 -	567.00	11/2013 -	-	.00	0
13	TIRUPATI - TIRUTHANI - CHENNAI - PPP (BOT) - [N24000178]	04/2011	571.00 -	571.00	10/2013 -	12/2017	.00	50
14	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - PPP (BOT) - [N24000185]	09/2011	574.00 -	574.00	03/2014 -	09/2017	.00	42
15	4-LANNING OF CHAPRA-HAJIPUR - PPP (ANNUITY) - [N24000187]	01/2011	575.00 -	575.00	07/2013 -	03/2018	.00	56
16	DEOLI KOTA - PPP (BOT) - [N24000148]	01/2011	593.00 -	593.00	07/2013 -	10/2017	.00	51

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs.150 Crore and above (October 2017)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
17	GWALIOR-JHANSI, NH-75 - PPP (ANNUITY) - [N24000089]	12/2003	604.00 -	604.00	12/2009 -	-	.00	0
18	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - PPP (BOT) - [N24000149]	02/2010	617.00 -	617.00	08/2012 -	12/2017	.00	64
19	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - PPP (ANNUITY) - [N24000213]	04/2012	624.00 -	624.00	04/2014 -	-	.00	0
20	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGPUR PPP (BOT) - [N24000586]	06/2016	637.18 -	637.18	06/2019 -	06/2019	.00	0
21	ROHTAK-BAWAL - PPP (BOT) - [N24000169]	05/2011	650.00 -	650.00	11/2013 -	08/2017	.00	45
22	2-LANNING WITH PS KHAGARIA-PURNEA - PPP (ANNUITY) - [N24000184]	05/2011	664.00 -	664.00	02/2014 -	-	.00	0
23	PATNA-MUZZAFFARPUR - PPP (ANNUITY) - [N24000165]	08/2010	671.30 -	671.30	02/2013 -	06/2018	.00	64
24	KRISHNANAGAR-BERHAMPUR - PPP (ANNUITY) - [N24000209]	02/2012	702.16 -	702.16	07/2014 -	03/2018	.00	44
25	MUZZAFFARNAGAR-HARIDWAR - PPP (BOT) - [N24000201]	09/2011	754.00 -	754.00	03/2013 -	11/2017	.00	56
26	FOUR LANING OF MAHUA TO KAGAVADAR OF NH- 8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - PPP (BOT) - [N24000587]	06/2016	763.23 -	763.23	06/2019 -	06/2019	.00	0
27	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - PPP (BOT) - [N24000445]	08/2014	822.90 -	822.90	04/2018 -	04/2018	.00	0
28	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - PPP (BOT) - [N24000500]	01/2016	830.36 -	830.36	07/2018 -	07/2018	.00	0
29	CHENGAPALLI TO COIMBATORE BYPASS KM- 102.035-144.740 KM - PPP (BOT) - [N24000144]	09/2010	852.00 -	852.00	03/2013 -	-	.00	51
30	BARSAT-KRISHNANAGAR - PPP (ANNUITY) - [N24000229]	08/2012	867.00 -	867.00	02/2015 -	12/2017	.00	34
31	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION PPP (BOT) - [N24000454]	06/2014	923.04 -	923.04	11/2016 -	11/2017	.00	12
32	KANDLA - MUNDRA PORT - PPP (BOT) - [N24000175]	01/2011	953.88 -	953.88	07/2013 -	-	.00	0
33	4 LANING OF SOLAPUR YEDISHI SECTION OF NH- 211 - PPP (BOT) - [N24000453]	01/2015	972.50 -	972.50	07/2017 -	01/2018	.00	6
34	4-LANING OF BRAHAMPUR-FARAKA - PPP (BOT) - [N24000203]	02/2011	998.79 -	998.79	08/2013 -	03/2018	.00	55
35	BAREILLY-SITAPUR (NH-24) - PPP (BOT) - [N24000200]	03/2011	1,046.00 -	1,046.00	09/2013 -	10/2017	.00	49

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs.150 Crore and above (October 2017)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
36	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - PPP (BOT) - [N24000205]	12/2011	1,047.00	1,047.00	06/2014	12/2017	.00	42
37	FOUR LANING OF GWALIOR-SHIVPURI - PPP (BOT) - [N24000494]	05/2013	1,055.00	1,601.77	11/2015	09/2017	51.83	22
38	4-LANING OF FARAKA-RAIGANJ - PPP (BOT) - [N24000202]	02/2011	1,078.84	1,078.84	08/2013	12/2017	.00	52
39	SRINAGAR TO BANIHAL - PPP (ANNUITY) - [N24000189]	06/2011	1,100.70	1,100.70	06/2014	12/2017	.00	42
40	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - PPP (BOT) - [N24000133]	05/2009	1,108.00	2,288.00	11/2011	03/2018	106.50	76
41	GHAZIABAD-ALIGARH NH-91 - PPP (BOT) - [N24000170]	02/2011	1,141.00	1,141.00	08/2013	08/2017	.00	48
42	INDORE-JHABUA-GUJRAT/MP - PPP (BOT) - [N24000136]	10/2010	1,175.00	1,206.10	04/2013	09/2017	2.65	53
43	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - PPP (BOT) - [N24000172]	09/2011	1,250.00	1,250.00	12/2013	12/2017	.00	48
44	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - PPP (BOT) - [N24000233]	04/2014	1,266.60	1,266.60	09/2016	03/2018	.00	18
45	MURADABAD-BAREILY - PPP (BOT) - [N24000154]	04/2010	1,267.00	1,267.00	06/2013	09/2017	.00	51
46	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - PPP (BOT) - [N24000230]	05/2013	1,348.20	1,348.20	02/2014	03/2018	.00	49
47	FOUR LANING OF HOSPET - CHITRADURGA - PPP (BOT) - [N24000490]	03/2015	1,388.00	1,388.00	-	08/2018	.00	0
48	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - PPP (BOT) - [N24000487]	07/2015	1,393.00	1,393.00	-	01/2018	.00	0
49	6-LANING OF DHANKUNI-KHARAGPUR SECTION - PPP (BOT) - [N24000206]	04/2012	1,396.18	1,396.18	09/2014	12/2017	.00	39
50	PANIKHOLI-RIMOLI - PPP (BOT) - [N24000197]	03/2012	1,410.00	1,410.00	09/2014	03/2018	.00	42
51	RANCHI-RARGA-JAMSETHPUR - PPP (ANNUITY) - [N24000215]	12/2012	1,479.00	1,479.00	06/2015	12/2017	.00	30
52	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - PPP (BOT) - [N24000125]	03/2010	1,509.10	3,237.87	09/2012	12/2017	114.56	63
53	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - PPP (BOT) - [N24000183]	11/2011	1,535.00	1,535.00	05/2014	06/2017	.00	37
54	ETAWAH CHAKERI - PPP (BOT) - [N24000219]	03/2013	1,573.00	1,573.00	09/2015	10/2017	.00	25
55	FOUR LANING OF BIAORA-DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - PPP (BOT) - [N24000505]	06/2015	1,583.79	1,583.79	-	01/2019	.00	0
56	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750- 356.502 KM - PPP (BOT) - [N24000145]	11/2010	1,585.00	1,585.00	05/2013	12/2017	.00	55

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs.150 Crore and above (October 2017)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
57	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - PPP (BOT) - [N24000462]	05/2014	1,655.01 -	1,655.01	08/2016 -	03/2018	.00	19
58	6 LANING OF AGRA - ETAWAH BYPASS - PPP (BOT) - [N24000452]	07/2015	1,657.20 -	1,657.20	- -	01/2019	.00	0
59	SIX-LANING OF BARWA ADDA-PANAGARH - PPP (BOT) - [N24000515]	04/2014	1,665.00 -	1,665.00	- -	12/2017	.00	0
60	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - PPP (BOT) - [N24000477]	02/2008	1,673.70 -	1,673.70	10/2011 -	12/2017	.00	74
61	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - PPP (BOT) - [N24000131]	02/2009	1,693.75 -	1,693.75	08/2011 -	09/2017	.00	73
62	PUNE-SATARA(NH-4) - PPP (BOT) - [N24000156]	10/2010	1,724.55 -	1,724.55	03/2013 -	12/2017	.00	57
63	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - PPP (ANNUITY) - [N24000163]	07/2010	1,813.76 -	1,813.76	07/2013 -	11/2017	.00	52
64	FOUR LANING OF AURANGABAD - YEDISHI - PPP (BOT) - [N24000508]	07/2015	1,871.34 -	1,871.34	01/2018 -	01/2018	.00	0
65	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - PPP (BOT) - [N24000232]	11/2013	1,916.79 -	1,916.79	11/2016 -	02/2018	.00	15
66	DELHI AGRA APPROVED LENGTH 180.0 KM - PPP (BOT) - [N24000224]	10/2012	1,928.22 -	1,928.22	04/2015 -	12/2017	.00	32
67	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - PPP (ANNUITY) - [N24000161]	07/2010	1,987.00 -	1,987.00	07/2015 -	03/2019	.00	44
68	AHMEDABAD TO VADODARA SECTION - PPP (BOT) - [N24000222]	01/2013	2,125.24 -	2,125.24	12/2015 -	07/2017	.00	19
69	8 LANING OF MUKARBA CHOWK TO PANIPAT - PPP (BOT) - [N24000449]	07/2015	2,128.72 -	2,128.72	- -	04/2019	.00	0
70	NASHRI- CHANANI - PPP (ANNUITY) - [N24000162]	05/2011	2,159.00 -	2,159.00	06/2015 -	-	.00	0
71	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - PPP (BOT) - [N24000425]	07/2015	2,288.18 -	2,288.18	- -	05/2019	.00	0
72	4 LANING OF NAGPUR-BETUL - PPP (ANNUITY) - [N24000155]	02/2011	2,498.76 -	2,498.76	08/2014 -	12/2017	.00	40
73	VARANASI-AURANGABAD KM.786 TO KM.978.40 - PPP (BOT) - [N24000182]	09/2011	2,848.00 -	2,848.00	03/2014 -	04/2018	.00	49
	Total		83,563.48 -	87,050.12				
	SHIPPING AND PORTS							
74	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - PPP (ANNUITY) - [N25000065]	10/2013	198.94 -	235.15	06/2017 -	-	18.20	0
75	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - PPP (ANNUITY) - [N25000066]	02/2015	244.50 258.00	258.33	12/2017 -	12/2017	5.66	0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs.150 Crore and above					(October 2017)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
76	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - PPP (BOT) - [N25000063]	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72	96
	Total		809.83 -	1,162.94				
	Grand Total		84,717.81	88,557.56				
