

**347th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(` 150 crore and above)
September 2014**



PORT TRUST - SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Abbreviations

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NGN	Next Generation Network
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

Contents

Executive Summary in English	1 -9
Month wise list of completed projects Costing Rs. 150 Crore and Above During 2013-14	10-11
Summary of Projects	12-25
Trend and Graphical Analysis of Projects	26-38
Sector wise analysis of projects	39-39
List of All Ongoing Projects	40-73
Sector wise Graph	74-85
ANNEXURE	86-86
Central Sector Projects	87-87
List of Projects Having Expenditure More than cost	88-97
List of Projects Ahead of Schedule	98-98
List of Projects with out Original date of Commissioning	99-100
List of Projects with out date of Commissioning	101-113
List of On schedule Projects Original Schedule	114-119
List of Delayed Projects w.r.t Original Schedule	120-138
List of Projects Having Time and cost overrun w.r.t original	139-143
List of Projects Having cost overrun w.r.t original	144-154

कार्यकारी सारांश

1. सितम्बर, 2014 की फ्लैश रिपोर्ट में `150 करोड़ और उससे अधिक लागत वाली केन्द्रीय क्षेत्र की 750 अवसंरचनात्मक परियोजनाओं की स्थिति दी गई है। सितम्बर, 2014 के दौरान नागर विमानन क्षेत्र के 2 परियोजनाओं के पूरा होने की सूचना दी गई है।
2. संदर्भाधीन माह के दौरान, 750 परियोजनाओं में से, 312 परियोजनाओं में मूल समय-सारणी की तुलना में विलंब हुआ तथा 49 परियोजनाओं के संबंध में पिछले माह में सूचित की गई समापन की तारीख की तुलना में अतिरिक्त विलंब की सूचना दी गई है। इन 49 परियोजनाओं में से, 17 परियोजनाएं `1000 करोड़ और अधिक लागत वाली बड़ी परियोजनाएं हैं।

क्र.सं.	क्षेत्र	निगरानी के तहत आने वाली परियोजनाएं	नवीनतम समय-सारणी की तुलना में विलंबित परियोजनाएं	रिपोर्ट वाले माह के दौरान अतिरिक्त विलंबित परियोजनाएं	अतिरिक्त विलंबित बड़ी परियोजनाएं
1.	रेलवे	291	32	11	5
2.	सड़क परिवहन एवं राजमार्ग	136	96	12	4
3.	विद्युत	102	56	2	0
4.	पेट्रोलियम	78	48	12	6
5.	कोयला	64	38	8	2
6.	शहरी विकास	25	13	0	0
7.	इस्पात	20	16	0	0
8.	पोत परिवहन एवं पत्तन	18	2	0	0
9.	नागर विमानन	6	4	2	0
10.	परमाणु ऊर्जा	4	4	0	0
11.	दूरसंचार	4	3	2	0
12.	पेट्रोरसायन	1	0	0	0
13.	जल संसाधन	1	0	0	0
कुल		750	312	49	17

3. 750 परियोजनाओं के कार्यान्वयन की कुल मूल लागत लगभग `9,47,912.88 करोड़ थी तथा उनके पूरा होने की अनुमानित लागत `11,25,673.75 करोड़ होने की संभावना है जो `1,77,760.87 करोड़ (मूल लागत का 18.80%) की समग्र लागत वृद्धि को दर्शाता है। सितम्बर, 2014 तक इन परियोजनाओं पर किया गया व्यय `5,23,833.51 करोड़ है जो परियोजनाओं की अनुमानित लागत का 46.50% है। लागतवृद्धि की अधिकतम प्रतिशतता वाली 5 परियोजनाएं नीचे दी गई हैं:-

लागतवृद्धि की अधिकतम प्रतिशतता वाली 5 परियोजनाओं की सूची (30.09.2014 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (करोड़)		लागत-वृद्धि (% में)
				मूल	अनुमानित	
1	नांगल बांध-तलवारा (एनएल), एनआर	रेलवे	03/1981	37.68	1036.78	2651.54
2	गाजोले-ईटाहार सहित इकलाखी-बलूरघाट से नई बी जी लाइन रेलवे लाइन (एनएल) एनईएफआर	रेलवे	04/1983	36.80	703.18	1810.82
3	बांकुरा-दामोदर (जीसी) (एसईआर)	रेलवे	03/1998	111.90	1423.98	1172.55
4	अकोला-खण्डवा जीसी अकोला-अकोट	रेलवे	04/2008	184.26	2000.00	985.42
5	बंगलोर सत्यमंगलम (एनएल) (एसडब्ल्यूआर)	रेलवे	02/1999	138.00	1382.78	902.01

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

4. वास्तविक अर्थ में अधिकतम लागतवृद्धि वाली 5 परियोजनाएं निम्नानुसार हैं:-

अधिकतम लागतवृद्धि वाली 5 परियोजनाओं की सूची(30.09.2014की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (₹ करोड़)		
				मूल लागत	अनुमानित लागत	लागत-वृद्धि
1	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	2500.00	19565.00	17065.00
2	कुसमुण्डा एक्सपे. (ओसीपी) (एसईसीएल) (15-50) एमटीवाई	कोयला	06/2008	1188.31	7612.33	6424.02
3	जिरीबाम से इंफाल (टीयूपीयूआई) (एनएल) (एनईएफआर)	रेलवे	04/2003	727.56	5996.00	5268.44
4	बंगलौर मेट्रो रेल परियोजना	शहरी विकास	05/2006	6395.00	11609.00	5214.00
5	पारादीप रिफाईनरी परियोजना	पेट्रोलियम	02/2009	29777.00	34555.00	4778.00

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

5. 750 परियोजनाओं में से, 8 परियोजनाएं समय से पहले चल रही हैं, 110 समय पर तथा 312 परियोजनाएं मूल समय-सारणी की तुलना में विलंबित हैं । तथापि, विलंबित परियोजनाओं की संख्या 289 तक और बढ़ जाती है यदि विलंब की गणना समापन की मूल समय-सारणी के आधार पर की जाती है । इसके अलावा, 18 परियोजनाएं किसी आरंभ संबंधी समय-सारणी/तारीख के बिना स्वीकृत की गई हैं तथा 302 परियोजनाओं के संबंध में न तो शुरू करने का वर्ष और न परियोजना के अंतरिम रूप से पूरा होने की अवधि सूचित की गई है । 312 विलंबित परियोजनाओं में से, 64 परियोजनाओं में 1 से 12 माह तक का विलंब हुआ, 75 परियोजनाओं में 13 से 24 महीने तक का विलंब हुआ, 101 परियोजनाओं में 25 से 60 माह तक का विलंब हुआ तथा 72 परियोजनाओं में 61 माह और उससे अधिक का विलंब हुआ । अधिकतम विलंब वाली 5 परियोजनाएं नीचे दी गई हैं:-

अधिकतम समयवृद्धि वाली 5 परियोजनाओं की सूची (30.09.2014की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	शुरू करने की तारीख		समय-वृद्धि (महीने में)
				मूल	अनुमानित	
1	गुना-इटावावाया शिवपुरी-ग्वालियर-भिंड एनएल (एनसीआर)	रेलवे	04/1986	03/1994	10/2014	247
2	फ्रैंट आप्रेशन्स इन्फोर्मेशन सिस्टम (एफओआईएस)	रेलवे	03/1984	03/1995	03/2015	240
3	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	11/2002	12/2018	193
4	बेलापुर-सीवूड-यूरान इलेक्ट्रीफाइड डबल लाईन (एमटीपी)	रेलवे	03/1996	03/2004	03/2016	144
5	रांची लोहरदग्गा (जीसी), एसईआर	रेलवे	04/1997	06/2004	12/2015	138

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक समयवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

6. अप्रैल, 2014 में इस मंत्रालय के प्रबोधन पर 727 परियोजनाओं में से 235 परियोजनाओं के संबंध में लागतवृद्धि तथा 282 परियोजनाओं के संबंध में समयवृद्धि की सूचना दी गई है; जबकि सितम्बर 2014 के दौरान 750 परियोजनाओं में से 215 परियोजनाओं के संबंध में लागतवृद्धि तथा 312 परियोजनाओं के संबंध में समयवृद्धि की सूचना दी गई है । अप्रैल 2014 की तुलना में लागतवृद्धि की सूचना देने वाली परियोजनाओं की संख्या 32% से घटकर 29% हो गई है जबकि समयवृद्धि की सूचना देने वाली परियोजनाओं की संख्या में मामूली वृद्धि 39% से 42% हो गई है व (अनुबंध 6 (क) तथा 6(ख) ।

7. विभिन्न अन्य परियोजना कार्यान्वयन एजेंसियों द्वारा यथा सूचित समयवृद्धि के संक्षिप्त कारणों में भूमि अधिग्रहण में विलंब, वन संबंधी अनुमति में विलंब, उपस्करों की आपूर्ति में विलंब, निधि की कमी, भू वैज्ञानिक गतिविधियां, उपस्कर स्थापित करने में समस्या, भूखनन की स्थिति, सिविल कार्यों में धीमी प्रगति, श्रम की कमी, ठेकेदार द्वारा अपर्याप्त संसाधन जुटाना, माओवादी समस्याएं, न्यायालय

मामले,संविदात्मक मुद्दे,आरओयू/आरओडब्ल्यू समस्याएं, कानून और व्यवस्था की स्थिति, आदि शामिल हैं ।

8. मंत्रालय के ऑनलाइन कम्प्यूटरीकृत मॉनीटरिंग सिस्टम (ओसीएमएस) में विभिन्न अवसंरचना परियोजनाओं के पीईआरटी चार्टों से तैयार किए गए लक्ष्यों की निगरानी की परिकल्पना की गई है । परियोजना प्राधिकारियों से नियमित रूप से अनुरोध किया गया है कि वे बेहतर निगरानी को सुचारू बनाने के लिए प्रत्येक परियोजना के संबंध में उपलब्धियों की सूची की प्रविष्टि करें । तथापि, सभी परियोजना एजेंसियां उपलब्धियों की सूची प्रदान नहीं कर रही हैं । पहले शुरू की गई 5 परियोजनाएं जिनके लक्ष्य परियोजना एजेंसियों द्वारा प्रदान नहीं किए जा रहे हैं, नीचे दी गई हैं:-

बिना उपलब्धियों वाली पहली 5 परियोजनाओं की सूची (30.09.2014 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (रु.करोड़)		संचयी व्यय (रु.करोड़)	शुरू करने की तारीख		उपलब्धि
				मूल	अनुमानित		मूल	अनुमानित	
1	हावड़ा-आमता-चंपादंगा एनएल (एससीआर)	रेलवे	04/1974	31.42	535.40	176.52	03/2007	03/2015	एन.आर.
2	नांगल बांध तलवारा (एनएल), एनआर	रेलवे	03/1981	37.68	1036.78	353.41	07/2012	एनआर	एन.आर.
3	इकलाखी-बलूरघाट से नई बी जी रेलवे लाइन	रेलवे	04/1983	36.80	703.17	247.74	एनआर	03/2015	एन.आर.
4	फ्रैंट आप्रेशनस इन्फोर्मेशन सिस्टम (एफओआईएस)	रेलवे	03/1984	520.00	634.13	555.27	03/1995	03/2013	एन.आर.
5	तामलुक दीघा, लाइन का दोहरीकरण (एसईआर)	रेलवे	03/1984	293.97	1074.47	433.89	06/2005	06/2016	एन.आर.

एन.आर.: सूचित नहीं ।

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार लक्ष्यों को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

9. यह भीपाया गया है कि परियोजना एजेंसियां संशोधित लागत अनुमानों तथा अनेक परियोजनाओं को शुरू करने की समय-सारणी को सूचित नहीं कर रही हैं, जो संकेत देता है कि समय/लागतवृद्धि संबंधी आंकड़े कम बताए गए हैं। पहले शुरू की गई 5 परियोजनाएं जिनमें परियोजना एजेंसियां संशोधित लागत अनुमानों की सूचना नहीं दे रही हैं/प्रदान नहीं करा रही हैं, नीचे दी गई हैं:-

बिना संशोधित लागत अनुमानों वाली पहली 5 परियोजनाओं की सूची (30.09.2014 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (₹ करोड़)		संचयी व्यय (₹ करोड़)
				मूल	संशोधित	
1	विरमगम-भिल्डी (डब्ल्यूआर), जीसी	रेलवे	04/1990	155.66	एनआर	200.42
2	शापुर-सरादिया और सोमनाथ-कोडिनार के लिए राजकोटवेरावल, वंशजालिया से जतलसर नए एमएम के साथ (जीसी)	रेलवे	04/1994	320.66	एनआर	462.18
3	पेड़ापल्ली-करीमनगर-निजामाबाद एनएल (एससीआर)	रेलवे	12/1994	124.43	495.68	688.63
4	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	2500.00	2500.00	8805.00
5	दल्ली-रजहारा रौघट (दल्ली-रजहारा जगदलपुर के भाग), एनएल, आरवीएनएल	रेलवे	04/1995	304.00	एनआर	138.39

एन.आर.: सूचित नहीं।

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार संशोधित लागत अनुमानों को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

पहले शुरू की गई 5 परियोजनाएं जिनमें परियोजना एजेंसियां शुरू करने की संशोधित समय-सारणी की सूचना नहीं दे रही हैं/प्रदान नहीं करा रही हैं, नीचे दी गई हैं:-

शुरू करने की संशोधित समय-सारणी के बिना पहली 5 परियोजनाओं की सूची (30.09.2014 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना को शुरू करने की तारीख		
				मूल	संशोधित	अनुमानित
1	नांगल बांध-तलवारा (एनएल), एनआर	रेलवे	03/1981	07/2012	एनआर	एनआर
2	विरमगाम-भिल्डी (डब्ल्यूआर), जीसी	रेलवे	04/1990	एनआर	03/2010	एनआर
3	अमरावती-नरखेर एनएल (सीआर)	रेलवे	06/1994	06/1999	03/2011	03/2011
4	पेड़ापल्ली-करीमनगर-निजामाबाद एनएल (एससीआर)	रेलवे	12/1994	एनआर	एनआर	03/2012
5	कोटूर-हरीहर (एनएल), (एसडब्ल्यूआर)	रेलवे	04/1995	एनआर	एनआर	12/2012

एन.आर.: सूचित नहीं ।

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार शुरू करने की संशोधित समय-सारणी को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

10. विलंब/अतिरिक्त विलंब का क्षेत्र-वार ब्यौरा निम्नानुसार है:-

- विद्युत क्षेत्र में, 102 परियोजनाओं में से 56 परियोजनाएं विलंबित हैं । माह के दौरान, 2 परियोजनाओं के संबंध में 1 तथा 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । परियोजना 'उत्तरी क्षेत्र की व्यवस्था का सुदृढीकरण योजना-XXIV, पीजीसीआईएल' में भूखनन तथा पर्यावरण संबंधी अनुमति में विलंब के कारण 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; और परियोजना 'डब्ल्यूआर तथा एनआर के लिए सामान्य व्यवस्था का सुदृढीकरण (लाईन बेज तथा रिएक्टर प्रावधान), पीजीसीआईएल' में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है)।

- ii) **नागर विमानन क्षेत्र में,** 6 परियोजनाओं में से 4 परियोजनाएं विलंबित हैं । माह के दौरान, 2 परियोजनाओं के संबंध में 1 तथा 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । परियोजना 'नए अंतर्राष्ट्रीय टर्मिनल भवन का निर्माण (गोवा), एएआई' में संस्थान के संरचनात्मक डिजाइन में परिवर्तन तथा संविदात्मक मुद्दे के कारण 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; तथा परियोजना 'विभिन्न हवाई अड्डों पर 56 संख्या एयरफील्ड फायर टैंडर की आपूर्ति, एएआई' में निविदा प्रक्रिया में विलंब के कारण 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।
- iii) **दूरसंचार क्षेत्र में,** 4 परियोजनाओं में से 3 परियोजनाएं विलंबित हैं । माह के दौरान, 2 परियोजनाओं के संबंध में 2 तथा 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । परियोजना 'टर्नकी आधार पर बीएसएनएल में ईआरपी कार्यान्वयन, बीएसएनएल' में निविदा संबंधी मुद्दे के कारण 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; तथा परियोजना 'उत्तरांचल में 283000 लाईनों (2जी) तथा 75000 लाईनों (3जी) का जीएसएम उपकरण, बीएसएनएल' में भूमि अधिग्रहण में विलंब के कारण अतिरिक्त विलंब की सूचना प्राप्त हुई है ।
- iv) **कोयला क्षेत्र में,** 64 परियोजनाओं में से 38 परियोजनाएं विलंबित हैं । माह के दौरान, 8 परियोजनाओं के संबंध में 1-36 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें से 2 मेगा परियोजनाएं हैं । परियोजना 'तूतीकोरिन थर्मल विद्युत परियोजना-2X500 मे.वा., एनएलसी' तथा 'विंड विद्युत परियोजना, काझुनीरकुलाम, तमिलनाडु, एनएलसी' में क्रमशः ठेकेदार द्वारा अपर्याप्त संसाधन जुटाने तथा भूमि अधिग्रहण में विलंब के कारण प्रत्येक में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई हैं; परियोजना कल्याणीखानी ओपनकास्ट परियोजना, एससीसीएल' में भूमि अधिग्रहण में विलंब के कारण 8 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'अदरियाला शाफ्ट परियोजना, एससीसीएल' में उपस्करों की आपूर्ति में विलंब के कारण 11 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'मानुगुरा ओसी-II विस्तार चरण-II, एससीसीएल' तथा 'आरजी ओसी-III, विस्तार (चरण-II) परियोजना, एससीसीएल' में वन संबंधी अनुमति में विलंब के कारण प्रत्येक में 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; तथा परियोजनाएं 'किस्ताराम ओसीपी, एससीसीएल' तथा 'जलगाम वेनगाला राव ओसीपी-II, एससीसीएल' में क्रमशः भूमि अधिग्रहण में विलंब तथा वन संबंधी भूमि के परिवर्तन में विलंब के कारण प्रत्येक में 36 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।

v) **रेलवे क्षेत्र** में, 291 परियोजनाओं में से 32 परियोजनाएं विलंबित हैं । माह के दौरान, 11 परियोजनाओं के संबंध में 1-51 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें से 5 मेगा परियोजनाएं हैं । परियोजनाएं गुलबर्ग-बिदार, एससीआर (एनएल), एससीआर तथा 'उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर' में निधि की कमी के कारण 1 तथा 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'रांची-लोहरदगा (जीसी), एसईआर' में कानून तथा व्यवस्था की समस्याओं के कारण 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'बोगिबिल तथा लिंक लाईनों पर ब्रह्मपुत्र पुल, एनईएफआर' में 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'अगरतला सबरूम, एनएल, एनईएफआर', 'अमबारी फलकाटा नई मायानगरी, एनईएफआर' तथा 'पेन रोहा दोहरीकरण, सीआर' प्रत्येक में 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'मनोहरपुर-बोंदामुंदा तीसरी लाईन दोहरीकरण, एसईआर' में 21 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'बारानगर से बराकपुर तथा दक्षिणेश्वर तक मेट्रो रेलवे के निर्माण हेतु नया कार्य (एमटीपी), आरवीएनएल' तथा 'बहुविध परिवहन व्यवस्था (एमएमटीएस) चरण-II हैदराबाद, एमआरटीपी' प्रत्येक में 24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; तथा परियोजना 'सेवोक रंगपो, एनईएफआर' में 51 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

vi) **पेट्रोलियम क्षेत्र** में, 78 परियोजनाओं में से 48 परियोजनाएं विलंबित हैं । माह के दौरान, 12 परियोजनाओं के संबंध में 1-68 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें से 6 मेगा परियोजनाएं हैं । परियोजनाएं 'पारादीप रिफाइनरी परियोजना, आईओसीएल' तथा '2000 एचपी ड्रिलिंग आरआईजी के 2 संख्या की खरीद, ऑयल' में क्रमशः भूमि अधिग्रहण में विलंब तथा संविदात्मक मुद्दों के कारण प्रत्येक में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं '102 मेगावाट विंड विद्युत परियोजना, ओएनजीसी' तथा 'बीपीसीएल/एचपीसीएल से यूरान एलपीजी संयंत्र तक एलपीजी के हस्तांतरण हेतु पाईपलाइन, बीपीसीएल में क्रमशः रक्षा मंत्रालय से अनापत्ति प्रमाण-पत्र मिलने में हुए विलंब तथा वैधानिक मंजूरी में हुए विलंब के कारण प्रत्येक में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'गैस टर्बाइन जनरेशन सेट, ऑयल' में सामग्रियों की आपूर्ति में विलंब के कारण 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'विजयपुर तथा पाटा में पेट्रोरसायन कॉम्प्लेक्स-II, गेल' में ठेकेदार के वित्तीय संकटों के कारण 5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'बी-127 क्षेत्रों का एकीकृत विकास, ओएनजीसी' तथा 'एनबीपी क्षेत्र (डी-1) के एनबीपी-14 ब्लॉक में लोअर पेज के लिए विकास योजना, ओएनजीसी' प्रत्येक में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है;

परियोजनाएं 'विसाखरिफाईनरीमेंडीजल हाइड्रोटेटर परियोजना, एचपीसीएल' तथा 'एमएच साउथ फील्ड के पश्चिमी परिधिका विकास, ओएनजीसी' में क्रमशः 4 तथा 5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; तथा परियोजनाएं 'जगदीशपुर-हल्दिया पाईपलाइन परियोजना चरण-I, गेल' तथा 'सूरत पारादीप पाईपलाइन परियोजना, गेल' में क्रमशः 38 तथा 68 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

vii) सड़क क्षेत्र में, 136 परियोजनाओं में से 96 परियोजनाएं विलंबित हैं । माह के दौरान, 12 परियोजनाओं के संबंध में 2-15 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें से 4 मेगा परियोजनाएं हैं । परियोजना 'एनएच 8डी के जेतपुर सोमनाथ सेक्शन की चार लेनिंग करना, लंबाई 127.6 कि.मी., एनएचएआई' में भूमि अधिग्रहण में विलंब तथा न्यायालय मामलों के लंबित होने के कारण 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'क्वाजीगुंड-बनिहाल 220.00 कि.मी. से 188.00 कि.मी. एनएसआई' तथा 'नशरी चनानी, एनएसआई' में क्रमशः ठेकेदार के निधि की कमी तथा भूमि अधिग्रहण के कारण प्रत्येक में 11 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'बेलगॉम-धारवाड़ (एनएच-4), एनएचएआई', नागपुर-वायनगंगा पुल, एनएचएआई', 'पीएसकानपुर कबरई के साथ 2 लेनिंग करना, एनएचएआई' तथा 'रीनगुस सिकार, एनएचएआई' प्रत्येक में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'संबलपुर-बारगढ़-छत्तीसगढ़/उड़ीसा बॉर्डर, एनएचएआई' तथा 'नौगांवसे धरमतुल (एएस-2), एनएचएआई' में क्रमशः 3 तथा 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'मुजफ्फरपुर-बरौनी के पेव्ड शॉल्डर के साथ 2 लेनिंग करना, एनएचएआई' तथा 'पनीखोली-रिमोली, एनएचएआई' में क्रमशः 8 तथा 13 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; तथा परियोजना 'बेवार-पाली-पिंदवाड़ा, एनएचएआई' में 15 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

11. दिनांक 30.09.2014 की स्थिति के अनुसार, विभिन्न क्षेत्रों में `150 करोड़ तथा अधिक लागत वाली परियोजनाओं के संबंध में स्थिति रिपोर्ट में सूचित की गई है ।
12. इसे सचिव, सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय का अनुमोदन प्राप्त है ।

EXECUTIVE SUMMARY

1. The Flash Report for September 2014 contains information on the status of the 750 Central Sector Infrastructure Projects costing ₹150 crore and above. During September 2014, 2 projects of Civil Aviation Sector have reported completion.

2. During the reference month, out of 750 projects, 312 projects are delayed with respect to original schedule and 49 projects have reported additional delays vis-à-vis the date of completion reported in the previous month. Of these 49 projects, 17 are Mega Projects costing ₹1000 crore and above.

S. No.	Sector	Projects on monitor	Delayed Projects w.r.t original schedule	Additionally delayed during the month under report	Additionally delayed Mega Projects
1.	RAILWAYS	291	32	11	5
2.	ROAD TRANSPORT AND HIGHWAYS	136	96	12	4
3.	POWER	102	56	2	0
4.	PETROLEUM	78	48	12	6
5.	COAL	64	38	8	2
6.	URBAN DEVELOPMENT	25	13	0	0
7.	STEEL	20	16	0	0
8.	SHIPPING AND PORTS	18	2	0	0
9.	CIVIL AVIATION	6	4	2	0
10.	ATOMIC ENERGY	4	4	0	0
11.	TELECOMMUNICATIONS	4	3	2	0
12.	PETROCHEMICALS	1	0	0	0
13.	WATER RESOURCES	1	0	0	0
Total		750	312	49	17

3. Total original cost of implementation of the 750 projects was ₹9,47,912.88 crore and their anticipated completion cost is likely to be ₹11,25,673.75 crore, which reflects overall cost overruns of ₹1,77,760.87 crore (18.80 % of original cost). The expenditure incurred on these projects till September 2014 is ₹5,23,833.51 crore, which is 46.50 % of the anticipated cost of the projects. The 5 projects with the maximum percentage cost overruns are as follows:-

LIST OF 5 PROJECTS HAVING MAXIMUM PERCENTAGE COST OVERRUNS(as on 30-09-2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹; crore)		COST OVERRUNS (in %)
				ORIGINAL	ANTICIPATED	
1	NANGALDAM-TALWARA(NL),NR	RAILWAYS	03/1981	37.68	1036.78	2651.54
2	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	RAILWAYS	04/1983	36.80	703.18	1810.82
3	BANKURA - DAMODAR (GC) (SER)	RAILWAYS	03/1998	111.90	1423.98	1172.55
4	AKOLA-KHANDWA GC AKOLA-AKOT	RAILWAYS	04/2008	184.26	2000.00	985.42
5	BANGLORE SATYAMANGALAM (NL)(SWR)	RAILWAYS	02/1999	138.00	1382.78	902.01

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

4. The 5 projects with maximum cost overruns in absolute terms are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM COST OVERRUNS(as on 30-09-2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹; crore)		
				ORIGINAL	ANTICIPATED	COST OVERRUNS
1	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	RAILWAYS	03/1995	2500.00	19565.00	17065.00
2	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY	COAL	06/2008	1188.31	7612.33	6424.02
3	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	RAILWAYS	04/2003	727.56	5996.00	5268.44
4	BANGALORE METRO RAIL PROJECT	URBAN DEVELOPMENT	05/2006	6395.00	11609.00	5214.00
5	PARADIP REFINERY PROJECT	PETROLEUM	02/2009	29777.00	34555.00	4778.00

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

5. Out of the 750 projects, 8 projects are ahead of schedule, 110 are on schedule and 312 are delayed with respect to original schedule. However, the number of delayed projects decreases to 289 if delay is calculated on the basis of latest schedule of completion. Further, 18 projects have been sanctioned without any commissioning schedule/date and for 302 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 312 delayed projects, 64 projects have overall delay in the range of 1 to 12 months, 75 projects have delay in

the range of 13 to 24 months, 101 projects have delay in the range of 25 to 60 months and 72 projects have delay of 61 months and above. The 5 projects with the maximum delay are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM TIME OVERRUNS (as on 30-09-2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	DATE OF COMMISSIONING		TIME OVERRUNS(in months)
				ORIGINAL	ANTICIPATED	
1	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	RAILWAYS	04/1986	03/1994	10/2014	247
2	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	RAILWAYS	03/1984	03/1995	03/2015	240
3	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	RAILWAYS	03/1995	11/2002	12/2018	193
4	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	RAILWAYS	03/1996	03/2004	03/2016	144
5	RANCHI-LOHARDAGA(GC),SER	RAILWAYS	04/1997	06/2004	12/2015	138

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further time overruns.

6. In April 2014, out of 727 projects on the monitor of this Ministry, 235 projects reported cost overruns and 282 projects reported time overruns; while during September 2014, out of 750 projects, 215 projects reported cost overruns and 312 projects reported time overruns. In comparison to April 2014, number of projects reporting cost overruns has gone down from 32% to 29% whereas projects reporting time overruns have increased to 42% from 39% (Annexure 6 (a) & 6 (b)).

7. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in forest clearance, delay in supply of equipments, fund constraints, geological surprises, problems in equipment erection, geo-mining conditions, slow

progress in civil works, shortage of labour, inadequate mobilization by the contractor, maoist problems, court cases, contractual issues, ROU/ROW problems, law and order situation, etc.

8. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones drawn from the PERT Charts of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The earliest initiated 5 projects in which project agencies are not providing milestones are as follows:-

List of 5 Earliest Projects without Milestones(as on 30-09-2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹ ; crore)		CUMULATIVE EXPENDITURE (₹ ; crore)	DATE OF COMMISSIONING		MILESTONES
				ORIGINAL	ANTICIPATED		ORIGINAL	ANTICIPATED	
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	Railways	04/1974	31.42	535.40	176.52	03/2007	03/2015	N.R.
2	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	37.68	1036.78	353.41	07/2012	N.R.	N.R.
3	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT	Railways	04/1983	36.80	703.17	247.74	N.R.	03/2015	N.R.
4	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	Railways	03/1984	520.00	634.13	555.27	03/1995	03/2013	N.R.
5	TAMLUK DIGHA,LINE DOUBLING (SER)	Railways	03/1984	293.97	1074.47	433.89	06/2005	06/2016	N.R.

N.R.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up milestones.

9. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The earliest initiated 5 projects in which project agencies are not reporting/providing revised cost estimates are as follows:-

List of 5 Earliest Projects without Revised Cost Estimates (as on 30-09-2014)

S N	PROJECT	SECTOR	DATE OF APPROVA L	COST OF PROJECT (₹, crore)		CUMULATIVE EXPENDITURE (₹, crore)
				ORIGINAL	REVISED	
1	VIRAMGAM-BHILDI(WR),GC	RAILWAY S	04/1990	155.66	N.R.	200.42
2	RAJKOTVERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	RAILWAY S	04/1994	320.66	N.R.	462.18
3	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	RAILWAY S	12/1994	124.43	495.68	688.63
4	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	RAILWAY S	03/1995	2500.00	2500.00	8805.00
5	DALLI-RAJHARA-RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL	RAILWAY S	04/1995	304.00	N.R.	138.39

N.R.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised cost estimates.

The earliest initiated 5 projects in which project agencies are not reporting/providing or updating revised commissioning schedules are as below:-

List of 5 Earliest Projects without Revised Commissioning Schedule(as on 30.09.2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	DATE OF COMMISSIONING		
				ORIGINAL	REVISED	ANTICIPATED
1	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	07/2012	N.R.	N.R.
2	VIRAMGAM-BHILDI(WR),GC	Railways	04/1990	N.R.	03/2010	N.R.
3	AMRAVATI-NARKHER NL(CR)	Railways	06/1994	06/1999	03/2011	03/2011
4	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	12/1994	N.R.	N.R.	03/2012
5	KOTTUR-HARIHAR(NL),(SWR)	Railways	04/1995	N.R.	N.R.	12/2012

N.R.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised commissioning schedule.

10. The Sector-wise details of additional delays are as under:-

i) In the **Power Sector**, out of 102 projects, 56 projects are delayed. During the month 2 projects have reported additional delay of 1 and 4 months. The project 'Northern Region System Strengthening Scheme-XXIV, PGCIL' has reported additional delay of 4 months due to geomining and environment clearance; and the project 'System Strengthening Common for WR and NR (Line Bays AND Reactor Provision), PGCIL' has reported additional delay of 1 month (however, no specific reasons have been reported by the project implementing agency for the delay in this project).

ii) In the **Civil Aviation Sector**, out of 6 projects, 4 projects are delayed. During the month 2 projects have reported additional delays of 1 and 12 months. The project 'Construction of New International Terminal Building (Goa), AAI' has reported additional delay of 1 month due to change in structural design of foundation and contractual issue; and the project 'Supply of 56 Nos Airfield Fire Tenders at Various Airports, AAI' has reported additional delay of 12 months due to delay in tendering process.

iii) In the **Telecommunications Sector**, out of 4 projects, 3 projects are delayed. During the month, 2 projects have reported additional delay of 2 and 3 months. The project 'ERP Implementation in BSNL on Turnkey Basis, BSNL' has reported additional delay of 2 months due to tendering issue; and the project 'GSM Equipment of 283000 Lines (2G) and 75000 Lines (3G) in Uttaranchal, BSNL' has reported additional delay of 3 months due to delay in land acquisition.

iv) In the **Coal Sector**, out of 64 projects, 38 projects are delayed. During the month, 8 projects have reported additional delay in the range of 1-36 months, out of which 2 are Mega project. The projects 'Tuticorin Thermal Power Project- 2X500 MW, NLC' and 'Wind Power Project, Kazhuneerkulam, Tamilnadu, NLC' have reported additional delay of 1 month each due to inadequate mobilization by the contractor and delay in land acquisition respectively; the project 'Kalyanikhani Opencast Project, SCCL' has reported additional delay of 8 months due to delay in land acquisition; the project 'Adriyala Shaft Project, SCCL' has reported additional delay of 11 months due to delay in supply of equipments; the projects 'Manuguru OC-II Extension Phase-II, SCCL' and 'RG OC -III Extension (Phase -II) Project, SCCL' have reported additional delays of 12 months each due to delay in forest clearance; and the projects 'Kistaram OCP, SCCL' and 'Jalagam Vengala Rao OCP-II, SCCL' have reported additional delays of 36 months each due

to delay in land acquisition and delay in diversion of forest land respectively.

v) In the **Railway Sector**, out of 291 projects, 32 projects are delayed. During the month, 11 projects have reported additional delays in the range of 1-51 months, out of which 5 are Mega projects. The projects 'Gulbarga-Bidar, SCR(NL), SCR' and 'Udhampur-Srinagar-Baramulla(NL), NR' have reported additional delays of 1 and 12 months due to fund constraints; the project 'Ranchi-Lohardaga(GC), SER' has reported additional delay of 6 months due to law and orders problems; the project 'Brahmaputra Bridge at Bogibil and Link Lines, NEFR' has reported additional delays of 6 months; the projects 'Agartala Sabroom, NL, NEFR', 'Ambari Falakata New Maynaguri, NEFR' and 'Pen Roha Doubling, CR' have reported additional delays of 12 months each; the project 'Manoharpur-Bondamunda 3rd Line Doubling, SER' has reported additional delay of 21 months; the projects 'New Work for Construction of Metro Railway from Baranagar to Barrackpore and Dakshineswar (MTP), RVNL' and 'Multi Modal Transport System(MMTS) Phase-II Hyderabad, MRTD' have reported additional delays of 24 months each; and the project 'Sevoke Rangpo, NEFR' has reported additional delay of 51 months (however, no specific reasons have been reported by the project implementing agencies for the delay in these projects).

vi) In the **Petroleum Sector**, out of 78 projects, 48 projects are delayed. During the month, 12 projects have reported additional delays in the range of 1-68 months, out of which 6 are Mega projects. The projects 'Paradip Refinery Project, IOCL' and 'Purchase of 2 Nos. of 2000 HP Drilling RIG, OIL' have reported additional delay of 1 month each due to delay in land acquisition and contractual issues respectively; the projects '102 MW Wind Power Project, ONGC' and 'Pipeline For Transfer of LPG from BPCL/HPCL to Uran LPG Plant, BPCL' have reported additional delays of 2 months each due to delay in obtaining no objection certificate (NOC), which is awaited from Ministry of Defence and delay in statutory clearances respectively; the project 'Gas Turbine Generation Set, OIL' has reported additional delay of 4 months due to delay in supply of materials; the project 'Petrochemical Complex-II at Vijaypur and Pata, GAIL' has reported additional delay of 5 months due to financial crises of contractor; the projects 'Integrated Development of B-127 Fields, ONGC' and 'Development Plan for Lower Pays in NBP-14 Block of NBP Field (D-1), ONGC' have reported additional delays of 2 months each; the projects 'Diesel Hydrotreater Project at Visakh Refinery, HPCL' and 'Development of Western Periphery of MH South Field, ONGC' have reported additional delays of 4 and 5 months respectively; and the projects 'Jagdishpur-Haldia Pipeline Project Phase-I, GAIL' and 'Surat Paradip Pipeline Project, GAIL' have reported additional delays

of 38 and 68 months respectively (however, no specific reasons have been reported by the project implementing agencies for the delay in these projects).

vii) In the **Road Sector**, out of 136 projects, 96 projects are delayed. During the month 12 projects have reported additional delays in the range of 2-15 months, out of which 4 are Mega projects. The project '4 Laning of Jetpur-Somnath Section of NH 8D Length KM 127.6, NHAI' has reported additional delay of 6 months due to delay in land acquisition and pending of court cases; the projects 'Quazigund-Banihal KM.220.00 to KM.188.00, NHAI' and 'Nashri-Chanani, NHAI' have reported additional delays of 11 months each due to fund constraints of contractor and land acquisition respectively; the projects 'Belgaum-Dharwad (NH-4), NHAI', 'Nagpur-Wainganga Bridge, NHAI', '2 Laning with PS Kanpur Kabrai, NHAI' and 'Reengus-Sikar, NHAI' have reported additional delays of 2 months each; the projects 'Sambalpur-Bargarh-Chhatisgarh/Orissa Border, NHAI' and 'Nagaon to Dharamtul (AS-2), NHAI' have reported additional delays of 3 and 4 months respectively; the projects '2-Laning with Paved Shoulder of Muzaffarpur-Barauni, NHAI' and 'Panikholi-Rimoli, NHAI' have reported additional delays of 8 and 13 months respectively; and the project 'BEAWAR-PALI-PINDWARA, NHAI' has reported additional delay of 15 months (however, no specific reasons have been reported by the project implementing agency for the delay in these projects).


11. The status as on 30.09.2014 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

12. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

EXECUTIVE SUMMARY

Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	291	11
2	ROAD TRANSPORT AND HIGHWAYS	136	12
3	POWER	102	2
4	PETROLEUM	78	12
5	COAL	64	8
6	URBAN DEVELOPMENT	25	0
7	STEEL	20	0
8	SHIPPING AND PORTS	18	0
9	CIVIL AVIATION	6	2
10	ATOMIC ENERGY	4	0
11	TELECOMMUNICATIONS	4	2
12	PETROCHEMICALS	1	0
13	WATER RESOURCES	1	0
	Total	750	49

Sectoral break up of on-going infrastructure projects.

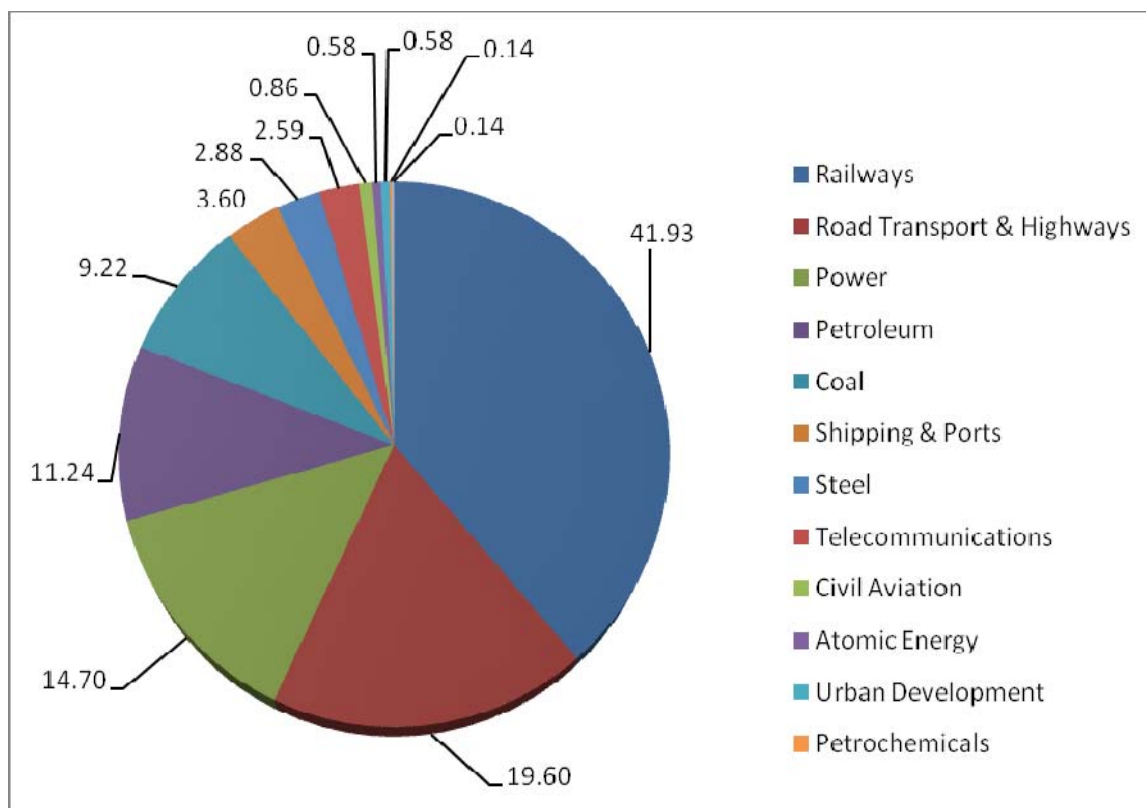

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2014-2015				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	May,2014			
	<u>COAL</u>			
1	BINA EXTN. PROJ(6.0 MTPA) (NORTHERN COAL FIELDS LIMITED) - [N06000019]	168.97	03/2014	67.53
	<u>POWER</u>			
2	PARBATI H.E.P. STAGE -III (NHPC) (NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [180100250]	2,304.56	10/2010	2,349.46
	June,2014			
	<u>PETROLEUM</u>			
3	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000039]	5,713.03	05/2010	3,918.86
4	DEVELOPMENT OF B-46 CLUSTER FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000046]	1,436.21	07/2010	1,165.53
5	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000060]	7,133.39	09/2012	2,795.50
	<u>POWER</u>			
6	MOUDA STTP (NATIONAL THERMAL POWER CORPORATION) - [N18000048]	5,459.28	08/2012	4,056.00
7	VINDHYACHAL STTP STAGE-IV (NATIONAL THERMAL POWER CORPORATION) - [N18000072]	5,915.00	10/2012	3,401.00
8	RIHAND STTP STAGE-III (2X500MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000073]	6,230.81	10/2012	4,357.00
	<u>RAILWAYS</u>			
9	CONSTRUCTION OF NEW LINE FROM HARMATI- ITANAGAR/NARHARIAGUN, NEFR (NORTH EAST FRONTIER RAILWAY) - [N22000083]	156.00	-	424.43
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
10	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106236]	166.27	03/2008	200.40
11	CHITRADURGA-TUMKUR(NH-4) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000157]	839.00	-	692.50
	July,2014			
	<u>STEEL</u>			

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2014-2015				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
12	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT EXP. UNIT (RASTRIYA ISPAT NIGAM LIMITED) - [N12000068]	202.00	01/2010	294.84
13	330 TPH BOILER-6 AND AUXILIARY SYSTEM (RASTRIYA ISPAT NIGAM LIMITED) - [N12000069]	260.00	12/2009	260.75
	<u>PETROLEUM</u>			
14	DEVELOPMENT OF C-SERIES FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000023]	3,195.16	12/2008	3,886.15
15	DEVELOPMENT OF B-22 CLUSTER FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000032]	2,323.40	09/2010	1,916.10
16	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000069]	3,284.00	09/2011	1,916.30
17	ADDITIONAL DEV. OF D-1 FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000086]	2,163.64	06/2012	2,182.31
	<u>POWER</u>			
18	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000106]	425.51	10/2013	386.32
	<u>TELECOMMUNICATIONS</u>			
19	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) PH-5.1 PUNJAB (BHARAT SANCHAR NIGAM LIMITED) - [N26000041]	373.94	12/2008	227.58
20	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK.PROCUREMENT OF GPON EQUIPMANT (BHARAT SANCHAR NIGAM LIMITED) - [N26000072]	952.88	03/2010	20.00
21	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK.PROCUREMENT OF GEPON EQUIPMENT (BHARAT SANCHAR NIGAM LIMITED) - [N26000073]	152.65	03/2010	29.05
22	GSM EQUIPMENT OF 799000LINES (2G) 101000 LINES 3(G) JHARKHANDPHASE V.1 TELECOM CIRCLE (BHARAT SANCHAR NIGAM LIMITED) - [N26000088]	328.13	03/2009	164.58
23	GSM EQUIPMENT OF 1625000LINES (2G) 325000 LINES 3(G) MP PHASE V.1 TELECOM CIRCLE (BHARAT SANCHAR NIGAM LIMITED) - [N26000090]	916.70	11/2010	828.48
	August,2014			
	<u>PETROLEUM</u>			
24	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I (GAS AUTHORITY OF INDIA LIMITED) - [N16000070]	238.68	01/2012	293.12
25	SINGLE POINT MOORING FACILITY(SMP) PROJECT (MANGALORE REFINERY AND PETROCHEMICALS LIMITED) - [N16000152]	1,043.57	04/2012	648.92
	<u>SHIPPING AND PORTS</u>			
26	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN (PORT TRUST) - [N25000048]	3,500.00	01/2012	3,661.95

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2014-2015				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	September,2014			
	<u>CIVIL AVIATION</u>			
27	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT (AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000037]	1,942.51	05/2011	2,573.92
28	D/O KAMARAJ DOMESTIC TER-PH-II AND EXP. ANNA INT. TER BLDG(K1) (AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000038]	1,808.00	01/2011	1,939.20


Summary of projects in the Flash Report for the month of September, 2014

Project Implementation - Current Status:

Number of Projects in Previous Month	720
Number of Projects completed/dropped/frozen in Current Month	2
Number of Projects Added in Current Month	32
Number of Projects in Current Month	750


Brief Analysis

Project Status with respect to Original Schedule: Out of 750 projects, 8 projects are ahead of schedule, 110 projects are on schedule and 312 projects are delayed. Of the balance, 302 projects do not have fixed dates of commissioning while 18 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

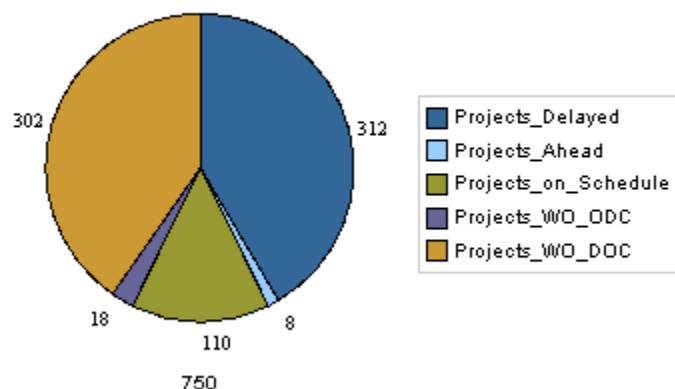

Investment Scenario

Total original cost of implementation of 750 projects when sanctioned, was of the order of Rs. 947912.88 crore but this was subsequently revised to Rs. 1125673.75 crore implying a cost overrun of 18.8%. The expenditure incurred on these projects till September, 2014 is Rs. 523833.51 crore, which is 46.5% of the revised cost of the projects.

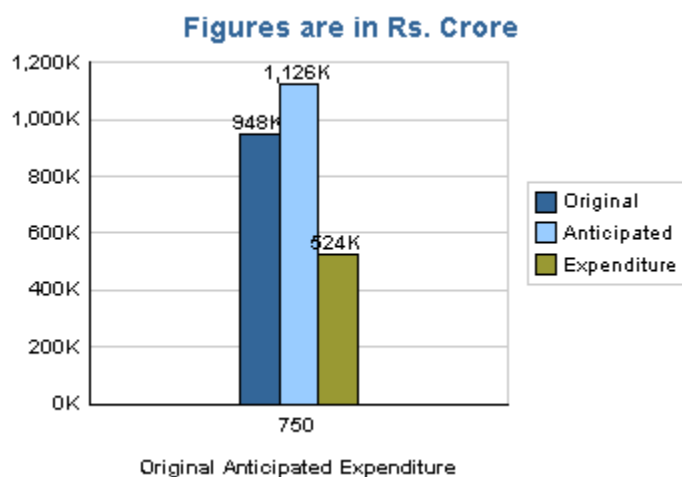

Projects Added / Completed / Dropped / Frozen

No of Projects in Previous Month	720
No of Projects Completed/Dropped/Frozen in Current Month	2
No of Projects added in Current Month	32
No of Projects in Current Month	750

Project status							
Number of Projects							
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total	Delayed Projects (%)
Original (Date)	312	8	110	18	302	750	41.60
Latest Approved (Date)	289	17	124	18	302	750	38.53

Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	662	7,85,532.80	8,71,513.75	3,66,262.23	42.00	85,980.95	10.90
Project with Revision in Cost	88	2,11,786.84	2,54,160.00	1,57,571.28	62.00	42,373.16	20.00
Total	750	9,97,319.64	11,25,673.75	5,23,833.51	46.54	128354.11	12.87
Original Cost of All Projects							
Original Cost	750	9,47,912.88	11,25,673.75	5,23,833.51	46.50	1,77,760.87	18.80

Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	312	550,384.33	652,164.21	400,612.58	61.40	101,779.88	18.50
Latest Approved (RCE)	290	550,871.28	610,960.12	380,271.88	62.20	60,088.84	10.90

Additional Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	49	96,852.89	128,360.95	72,857.72	56.80	31,508.06	32.50

Extent of cost overrun in projects with respect to original schedule(Sector Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overrun			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	2	16,663.00	22,947.00	37.71
2	CIVIL AVIATION	6	2,284.95	2,337.87	2.32	1	335.61	388.53	15.77
3	COAL	64	46,558.77	56,675.18	21.73	8	9,767.76	20,481.91	109.69
4	STEEL	20	66,395.10	72,349.06	8.97	4	23,538.89	29,522.85	25.42
5	PETROCHEMICALS	1	5,460.61	8,920.00	63.35	1	5,460.61	8,920.00	63.35
6	PETROLEUM	78	178,906.90	195,033.69	9.01	18	58,704.97	78,645.67	33.97
7	POWER	102	244,305.12	259,040.96	6.03	14	36,971.05	51,706.89	39.86
8	RAILWAYS	291	163,873.51	274,821.46	67.70	146	70,767.31	182,046.41	157.25
9	ROAD TRANSPORT AND HIGHWAYS	136	102,321.44	104,388.44	2.02	9	2,866.62	4,961.13	73.07
10	SHIPPING AND PORTS	18	12,117.12	14,390.98	18.77	8	5,128.97	7,707.06	50.27
11	TELECOMMUNICATIONS	4	2,018.15	1,843.90	-8.63	1	149.15	158.72	6.42
12	URBAN DEVELOPMENT	25	82,686.31	87,959.21	6.38	2	6,509.18	11,782.08	81.01
13	WATER RESOURCES	1	542.90	1,187.00	118.64	1	542.90	1,187.00	118.64
Total		750	947,912.88	1,125,673.75	18.75	215	237,406.02	420,455.25	77.10

Extent of cost overrun in projects with respect to original schedule(State Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overrun			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	22	24,992.52	30,169.08	20.71	7	10,837.36	16,880.92	55.77
2	ARUNACHAL PRADESH	3	9,356.22	12,067.66	28.98	2	3,070.89	5,782.33	88.29
3	ASSAM	38	26,930.69	41,738.17	54.98	16	13,341.92	28,238.59	111.65
4	BIHAR	48	37,027.18	43,648.73	17.88	14	13,719.68	20,561.55	49.87
5	GOA	1	335.61	388.53	15.77	1	335.61	388.53	15.77
6	GUJARAT	33	38,581.24	39,407.29	2.14	6	2,786.26	3,932.72	41.15
7	HARYANA	9	4,540.88	6,690.86	47.35	3	1,633.56	3,783.54	131.61
8	HIMACHAL PRADESH	6	13,728.27	19,787.64	44.14	3	9,493.62	15,552.99	63.83
9	JAMMU AND KASHMIR	7	21,314.62	40,235.30	88.77	2	6,142.04	25,062.72	308.05
10	KARNATAKA	34	78,337.98	92,917.96	18.61	17	13,700.79	28,532.51	108.25
11	KERALA	12	19,275.88	23,429.66	21.55	5	16,205.39	20,359.17	25.63
12	MADHYA PRADESH	17	23,452.88	24,921.57	6.26	4	2,144.95	4,033.08	88.03
13	MAHARASHTRA	47	71,517.57	83,936.57	17.37	14	16,502.42	29,117.29	76.44
14	MANIPUR	1	727.56	5,996.00	724.12	1	727.56	5,996.00	724.12
15	MEGHALAYA	3	4,845.02	4,845.02	0.00	0	0.00	0.00	0.00
16	MIZORAM	2	988.06	3,307.11	234.71	2	988.06	3,307.11	234.71
17	NAGALAND	2	5,124.00	6,720.57	31.16	1	850.00	2,446.57	187.83
18	ODISHA	41	67,166.05	75,819.10	12.88	11	32,706.66	41,359.71	26.46
19	PUNJAB	4	1,497.50	1,470.46	-1.81	0	0.00	0.00	0.00
20	RAJASTHAN	25	25,638.72	25,695.94	0.22	6	2,613.49	3,156.81	20.79
21	SIKKIM	2	1,648.94	3,684.88	123.47	1	1,339.48	3,375.42	151.99
22	TAMIL NADU	41	53,533.49	70,513.46	31.72	20	30,028.23	47,008.20	56.55
23	TRIPURA	6	2,966.26	4,780.63	61.17	3	2,129.35	3,978.10	86.82
24	UTTAR PRADESH	26	14,207.60	16,863.93	18.70	9	2,951.38	5,655.97	91.64
25	WEST BENGAL	39	55,626.19	63,977.61	15.01	9	21,601.69	29,953.12	38.66
26	CHANDIGARH	1	452.00	452.00	0.00	0	0.00	0.00	0.00
27	DELHI	9	44,464.60	44,464.60	0.00	0	0.00	0.00	0.00
28	CHHATISGARH	27	58,300.98	65,886.82	13.01	7	2,726.97	10,312.81	278.18
29	JHARKHAND	31	21,501.51	21,869.27	1.71	5	1,380.26	1,919.79	39.09
30	UTTARAKHAND	7	9,501.04	13,063.93	37.50	5	7,496.04	11,058.93	47.53
31	TELANGANA	21	9,410.31	12,179.13	29.42	5	1,473.01	4,241.83	187.97
32	MULTI STATE	185	200,921.51	224,744.27	11.86	36	18,479.35	44,458.94	140.59
Total		750	947,912.88	1,125,673.75	18.75	215	237,406.02	420,455.25	77.10

Extent of time overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	4	40,442.00	46,726.00	17 - 71
2	CIVIL AVIATION	6	2,284.95	2,337.87	2.32	4	1,206.95	1,259.87	10 - 71
3	COAL	64	46,558.77	56,675.18	21.73	38	29,523.97	40,059.98	1 - 120
4	STEEL	20	66,395.10	72,349.06	8.97	16	64,938.54	70,892.50	3 - 73
5	PETROCHEMICALS	1	5,460.61	8,920.00	63.35	0	0.00	0.00	-
6	PETROLEUM	78	178,906.90	195,033.69	9.01	48	120,041.33	133,821.78	2 - 110
7	POWER	102	244,305.12	259,040.96	6.03	56	186,803.25	201,159.31	1 - 106
8	RAILWAYS	291	163,873.51	274,821.46	67.70	32	28,509.69	76,350.68	3 - 247
9	ROAD TRANSPORT AND HIGHWAYS	136	102,321.44	104,388.44	2.02	96	67,308.76	69,375.76	2 - 120
10	SHIPPING AND PORTS	18	12,117.12	14,390.98	18.77	2	2,194.46	3,093.38	11 - 51
11	TELECOMMUNICATIONS	4	2,018.15	1,843.90	-8.63	3	869.96	879.53	53 - 71
12	URBAN DEVELOPMENT	25	82,686.31	87,959.21	6.38	13	8,545.42	8,545.42	2 - 55
13	WATER RESOURCES	1	542.90	1,187.00	118.64	0	0.00	0.00	-
Total		750	947,912.88	1,125,673.75	18.75	312	550,384.33	652,164.21	

9

Extent of time overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	3	36,950.00	41,049.00	17 - 71
2	CIVIL AVIATION	6	2,284.95	2,337.87	2.32	4	1,206.95	1,259.87	10 - 71
3	COAL	64	46,558.77	56,675.18	21.73	38	29,523.97	40,059.98	1 - 120
4	STEEL	20	66,395.10	72,349.06	8.97	16	64,938.54	70,892.50	3 - 73
5	PETROCHEMICALS	1	5,460.61	8,920.00	63.35	0	0.00	0.00	-
6	PETROLEUM	78	178,906.90	195,033.69	9.01	41	112,003.25	118,888.19	2 - 73
7	POWER	102	244,305.12	259,040.96	6.03	54	183,937.63	195,591.73	1 - 106
8	RAILWAYS	291	163,873.51	274,821.46	67.70	28	21,415.35	63,381.26	3 - 247
9	ROAD TRANSPORT AND HIGHWAYS	136	102,321.44	104,388.44	2.02	89	65,879.03	67,854.08	2 - 120
10	SHIPPING AND PORTS	18	12,117.12	14,390.98	18.77	1	1,228.00	2,098.56	51 - 51
11	TELECOMMUNICATIONS	4	2,018.15	1,843.90	-8.63	2	485.96	495.53	66 - 71
12	URBAN DEVELOPMENT	25	82,686.31	87,959.21	6.38	13	8,545.42	8,545.42	2 - 55
13	WATER RESOURCES	1	542.90	1,187.00	118.64	0	0.00	0.00	-
Total		750	947,912.88	1,125,673.75	18.75	289	526,114.10	610,116.12	

Extent of cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overruns			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	46,726.00	46,726.00	0.00	0	0.00	0.00	0.00
2	CIVIL AVIATION	6	2,284.95	2,337.87	2.32	1	335.61	388.53	15.77
3	COAL	64	51,201.03	56,675.18	10.69	6	5,647.69	12,650.78	124.00
4	STEEL	20	70,414.06	72,349.06	2.75	1	14,443.00	16,408.00	13.61
5	PETROCHEMICALS	1	5,460.61	8,920.00	63.35	1	5,460.61	8,920.00	63.35
6	PETROLEUM	78	197,614.03	195,033.69	-1.31	2	5,909.70	6,276.27	6.20
7	POWER	102	245,180.57	259,040.96	5.65	9	26,163.99	40,024.38	52.98
8	RAILWAYS	291	177,101.73	274,821.46	55.18	137	69,518.58	167,569.46	141.04
9	ROAD TRANSPORT AND HIGHWAYS	136	102,692.45	104,388.44	1.65	8	2,906.07	4,651.57	60.06
10	SHIPPING AND PORTS	18	13,337.95	14,390.98	7.90	6	4,617.63	5,882.10	27.38
11	TELECOMMUNICATIONS	4	2,018.15	1,843.90	-8.63	1	149.15	158.72	6.42
12	URBAN DEVELOPMENT	25	82,745.21	87,959.21	6.30	1	6,395.00	11,609.00	81.53
13	WATER RESOURCES	1	542.90	1,187.00	118.64	1	542.90	1,187.00	118.64
Total		750	997,319.64	1,125,673.75	12.87	174	142,089.93	275,725.81	94.05

Extent of time & cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	2	16,663.00	22,947.00	54- 71
2	CIVIL AVIATION	6	2,284.95	2,337.87	2.32	0	0.00	0.00	0- 0
3	COAL	64	46,558.77	56,675.18	21.73	3	8,165.59	11,154.87	32- 64
4	STEEL	20	66,395.10	72,349.06	8.97	3	9,095.89	13,114.85	39- 73
5	PETROCHEMICALS	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
6	PETROLEUM	78	178,906.90	195,033.69	9.01	8	38,382.60	53,582.05	8- 110
7	POWER	102	244,305.12	259,040.96	6.03	2	2,078.01	3,973.71	16- 94
8	RAILWAYS	291	163,873.51	274,821.46	67.70	4	5,980.91	9,532.05	36- 144
9	ROAD TRANSPORT AND HIGHWAYS	136	102,321.44	104,388.44	2.02	2	425.61	517.56	69- 80
10	SHIPPING AND PORTS	18	12,117.12	14,390.98	18.77	4	1,900.70	3,348.81	10- 99
11	TELECOMMUNICATIONS	4	2,018.15	1,843.90	-8.63	0	0.00	0.00	0- 0
12	URBAN DEVELOPMENT	25	82,686.31	87,959.21	6.38	0	0.00	0.00	0- 0
13	WATER RESOURCES	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		750	947912.88	1125673.75	18.75	28	82692.31	118170.9	

Extent of time & cost overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	2	16,663.00	22,947.00	54- 71
2	CIVIL AVIATION	6	2,284.95	2,337.87	2.32	1	335.61	388.53	29- 29
3	COAL	64	46,558.77	56,675.18	21.73	6	9,127.17	19,793.22	24- 120
4	STEEL	20	66,395.10	72,349.06	8.97	4	23,538.89	29,522.85	36- 73
5	PETROCHEMICALS	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
6	PETROLEUM	78	178,906.90	195,033.69	9.01	14	43,395.85	60,945.32	2- 110
7	POWER	102	244,305.12	259,040.96	6.03	12	34,823.04	48,634.19	10- 106
8	RAILWAYS	291	163,873.51	274,821.46	67.70	28	23,380.83	71,221.82	3- 247
9	ROAD TRANSPORT AND HIGHWAYS	136	102,321.44	104,388.44	2.02	9	2,866.62	4,961.13	40- 93
10	SHIPPING AND PORTS	18	12,117.12	14,390.98	18.77	2	2,194.46	3,093.38	11- 51
11	TELECOMMUNICATIONS	4	2,018.15	1,843.90	-8.63	1	149.15	158.72	66- 66
12	URBAN DEVELOPMENT	25	82,686.31	87,959.21	6.38	0	0.00	0.00	0- 0
13	WATER RESOURCES	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		750	947912.88	1125673.75	18.75	79	156474.62	261666.16	

List of projects completed/dropped/Frozen during current month							(All Cost /Expenditure in Rs. crore)
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>CIVIL AVIATION</u>						
1	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT	08/2008	1,942.51	05/2011	2,573.92	03/2013	2,573.92
2	D/O KAMARAJ DOMESTIC TER-PH-II AND EXP. ANNA INT. TER BLDG(K1)	08/2008	1,808.00	01/2011	2,015.00	05/2012	1,939.20

List of projects added					(All Cost in Rs. crore)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>COAL</u>					
1	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	5/2014	479.15	3/2019	479.15	3/2019
2	SIARMAL OCP (40.00MTY)	5/2014	3,756.36	3/2026	3,756.36	3/2026
3	JAGANNATH RE-ORGANISATION OC.(6.00 MTY)	5/2014	337.66	3/2019	337.66	3/2019
4	KULDA EXPN OC. (5.00 MTY)	6/2014	289.03	3/2018	289.03	3/2018
	<u>PETROLEUM</u>					
5	GUJARAT REGION PIPELINE REPLACEMENT PROJECT	7/2014	716.00	1/2017	716.00	1/2017
6	KG BASIN PIPELINE REPLACEMENT PROJECT	7/2014	762.00	1/2017	762.00	1/2017
7	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY	12/2011	160.00	3/2014	160.00	7/2016
	<u>POWER</u>					
8	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	10/2014	8,112.12	4/2020	8,112.12	4/2020
	<u>RAILWAYS</u>					
9	GHAZIPUR - AUNRIHAR (40 KM)	4/2014	182.92	/	197.73	-
10	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM)	4/2011	190.10	/	190.10	-

List of projects added					(All Cost in Rs. crore)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
11	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	4/2012	148.77	12/2016	174.69	12/2016
12	HOSADURGA - CHICKJAJUR (28.89 KM)	4/2010	203.40	/	203.40	-
	<u>URBAN DEVELOPMENT</u>					
13	CONSTRUCTION OF CENTRAL ACADEMY FOR PUBLIC TRAINING (CAPT) BHOPAL	12/2012	188.87	12/2014	188.87	12/2016
14	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM	4/2014	332.72	9/2016	332.72	9/2016
15	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA	1/2009	225.81	6/2012	225.81	5/2015
16	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	2/2014	156.57	9/2015	156.57	12/2016
17	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA	2/2012	171.10	9/2014	171.10	9/2014
18	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI	1/2010	162.90	7/2012	162.90	7/2012
19	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	11/2012	270.83	11/2014	270.83	10/2015
20	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB	11/2012	238.43	2/2015	238.43	8/2015
21	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD	9/2012	171.86	3/2016	171.86	5/2016
22	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	2/2011	241.33	11/2014	241.33	11/2014
23	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI	5/2009	261.85	5/2013	261.85	10/2015
24	C/O MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB	8/2005	191.24	8/2007	191.24	12/2010
25	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1,219.21	7/2017	1,219.21	7/2017
26	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARAstra	6/2010	205.00	3/2012	205.00	1/2015
27	C/O NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARAstra	12/2012	315.00	6/2015	315.00	8/2015
28	C/O MEGA HOSTEL II FOR NIT CALICUT KERALA	1/2010	165.23	10/2012	165.23	9/2013
29	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD	6/2014	157.84	3/2017	157.84	3/2017
30	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI	5/2012	405.01	12/2014	405.01	4/2016
31	DEVELOPMENT OF STATE HIGHWAYS IN THE	11/2006	2,727.89	3/2010	2,727.89	10/2014

List of projects added					(All Cost in Rs. crore)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	STATE OF BIHAR UNDER RSVY PATNA					
32	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	7/2012	884.30	8/2014	884.30	1/2016

Milestones (Cumulative due & achieved)		
Total	3741	
Achieved up to month	1429	


List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>CIVIL AVIATION</u>						
1	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) AAI	335.61	388.53	05/2012	09/2014	10/2014	1
2	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS AAI	217.60	217.60	03/2015	03/2015	03/2016	12
	<u>COAL</u>						
3	TUTICORIN THERMAL POWER PROJECT- 2X500 MW NLC	4,904.54	6,602.74	03/2012	10/2014	11/2014	1
4	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU NLC	364.75	364.75	10/2014	10/2014	11/2014	1
5	KALYANIKHANI OPENCAST PROJECT SCCL	417.33	417.33	07/2016	07/2016	03/2017	8
6	ADRIYALA SHAFT PROJECT SCCL	212.34	1,228.39	03/2013	10/2014	09/2015	11
7	MANUGURU OC-II EXTENSION PHASE-II SCCL	181.19	181.19	03/2012	03/2015	03/2016	12
8	RG OC -III EXTENSION (PHASE -II) PROJECT SCCL	365.01	365.01	06/2015	06/2015	06/2016	12
9	KISTARAM OCP SCCL	242.29	242.29	03/2015	03/2015	03/2018	36
10	JALAGAM VENGALA RAO OCP-II SCCL	447.06	447.06	03/2015	03/2015	03/2018	36
	<u>PETROLEUM</u>						
11	PARADIP REFINERY PROJECT IOCL	29,777.00	34,555.00	11/2012	02/2015	03/2015	1
12	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG OIL	270.00	270.00	12/2014	02/2016	03/2016	1
13	102 MW WIND POWER PROJECT ONGC	1,106.00	678.02	06/2012	10/2014	12/2014	2
14	INTEGRATED DEVELOPMENT OF B-127 FIELDS ONGC	2,059.63	2,665.65	03/2015	03/2015	05/2015	2
15	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT BPCL	246.81	276.83	08/2012	08/2014	10/2014	2
16	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) ONGC	429.06	429.06	10/2014	10/2014	12/2014	2

List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
17	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY HPCL	3,597.00	2,730.00	09/2011	07/2014	11/2014	4
18	GAS TURBINE GENERATION SET OIL	216.88	216.88	10/2011	08/2014	12/2014	4
19	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA GAIL	8,140.00	8,140.00	02/2014	10/2014	03/2015	5
20	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD ONGC	600.17	600.17	12/2014	12/2014	05/2015	5
21	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I GAIL	7,596.18	7,596.18	01/2013	12/2015	02/2019	38
22	SURAT PARADIP PIPELINE PROJECT GAIL	10,281.00	10,281.00	04/2015	04/2015	12/2020	68
	<u>POWER</u>						
23	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) PGCIL	213.78	213.78	03/2014	10/2014	11/2014	1
24	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV PGCIL	723.63	723.63	11/2014	11/2014	03/2015	4
	<u>RAILWAYS</u>						
25	GULBARGA-BIDAR,SCR(NL) SCR	242.42	844.00	N.A.	02/2015	03/2015	1
26	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR NEFR	1,500.00	4,996.19	04/2008	12/2016	06/2017	6
27	RANCHI-LOHARDAGA(GC),SER SER	194.07	334.90	06/2004	06/2015	12/2015	6
28	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR NR	2,500.00	19,565.00	11/2002	12/2017	12/2018	12
29	AGARTALA SABROOM, NL, NEFR NEFR	813.34	1,741.00	03/2014	03/2017	03/2018	12
30	AMBARI FALAKATA TO NEW MAYNAGURI NEFR	312.12	312.12	N.A.	03/2016	03/2017	12
31	PEN ROHA DOUBLING CR	98.74	203.00	N.A.	03/2014	03/2015	12
32	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING SER	258.20	315.13	N.A.	03/2016	12/2017	21
33	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) RVNL	2,298.42	2,298.42	03/2014	03/2014	03/2016	24


List of projects reporting additional delays

Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
34	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD MRTD	632.68	816.55	04/2012	03/2016	03/2018	24
35	SEVOK RANGPO, NEFR NEFR	1,339.48	3,375.42	12/2015	12/2015	03/2020	51
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
36	BELGAUM-DHARWAD(NH-4) NHAI	480.00	480.00	N.A.	08/2014	10/2014	2
37	NAGPUR-WAINGANGA BRIDGE NHAI	484.19	484.19	10/2014	10/2014	12/2014	2
38	2 LANING WITH PS KANPUR KABRAI NHAI	373.47	373.47	07/2014	09/2014	11/2014	2
39	REENGUS SIKAR NHAI	333.51	333.51	09/2014	09/2014	11/2014	2
40	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER NHAI	909.00	909.00	05/2014	09/2014	12/2014	3
41	NAGAON TO DHARAMTUL (AS-2) NHAI	264.72	264.72	06/2008	08/2014	12/2014	4
42	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 NHAI	828.00	828.00	09/2014	09/2014	03/2015	6
43	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI NHAI	356.40	356.40	07/2014	07/2014	03/2015	8
44	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 NHAI	1,987.00	1,987.00	07/2015	07/2015	06/2016	11
45	NASHRI CHANANI NHAI	2,159.00	2,159.00	06/2015	06/2015	05/2016	11
46	PANIKHOLI-RIMOLI NHAI	1,410.00	1,410.00	09/2014	09/2014	10/2015	13
47	BEAWAR-PALI-PINDWARA NHAI	2,388.00	2,388.00	06/2014	08/2014	11/2015	15
	<u>TELECOMMUNICATIONS</u>						
48	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS BSNL	384.00	384.00	10/2010	01/2015	03/2015	2
49	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTANCHAL BSNL	149.15	158.72	06/2009	09/2014	12/2014	3

Graphical Presentation of All Projects w.r.t. Original Schedule

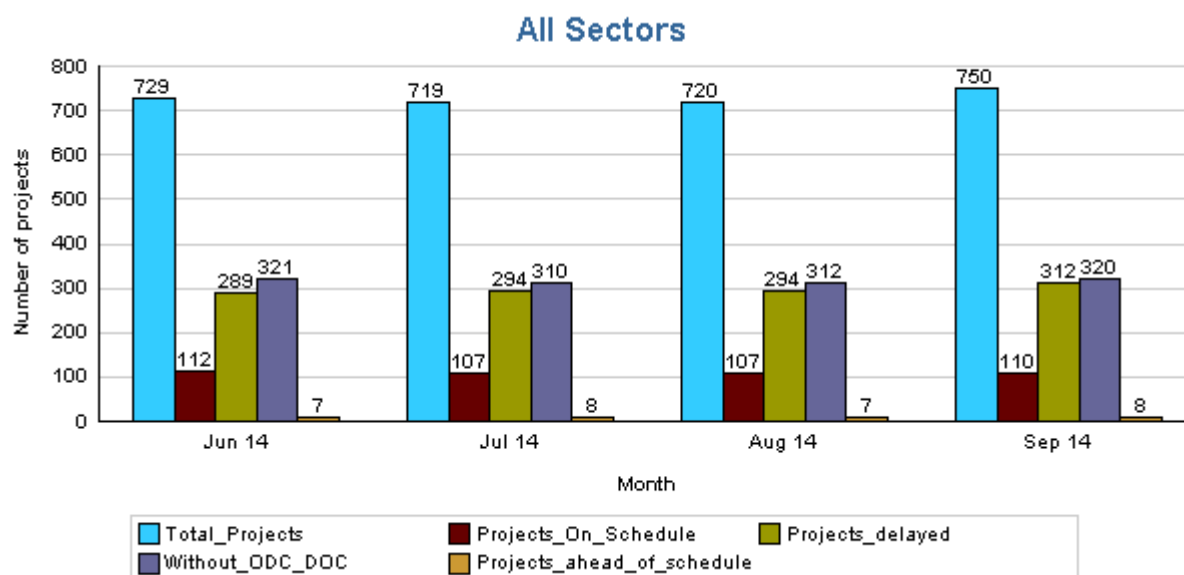

Break-up of 312 Delayed projects in September 2014

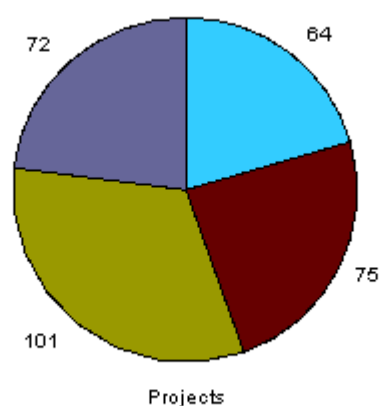


Delay in Months


Legend:

- 1-12
- 13-24
- 25-60
- MORE THAN 60

Graphical Presentation of All Projects w.r.t. Revised Schedule

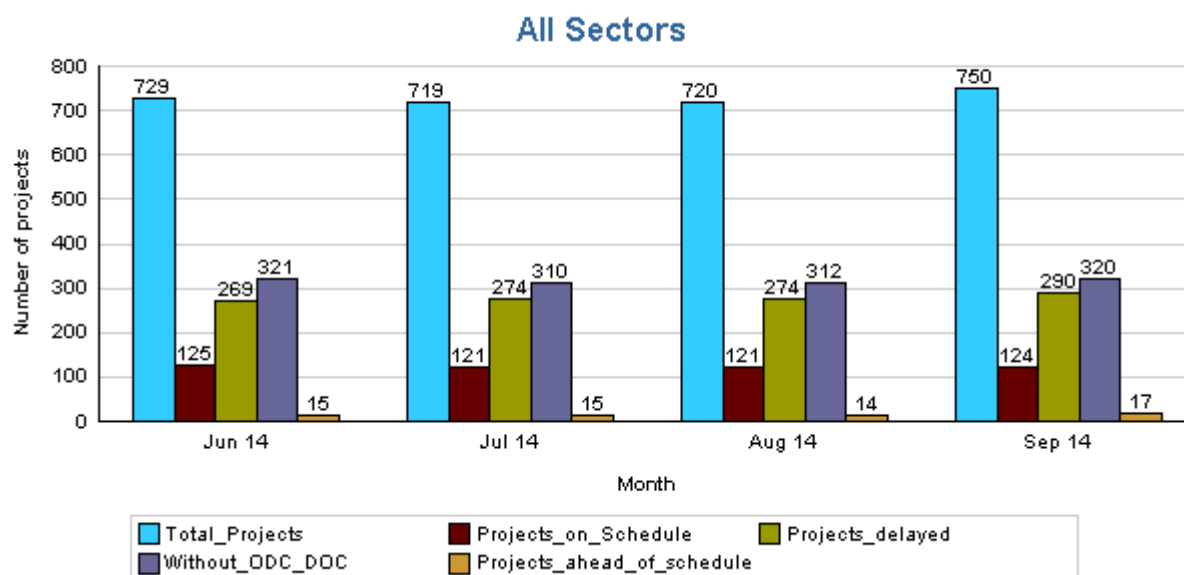


Break-up of 290 Delayed projects in September 2014

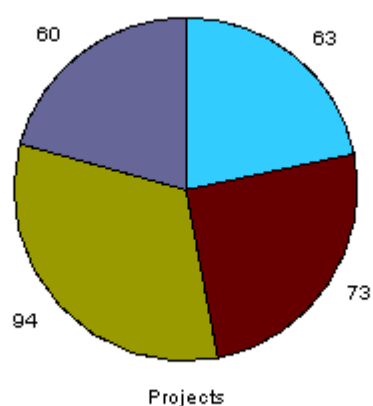


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

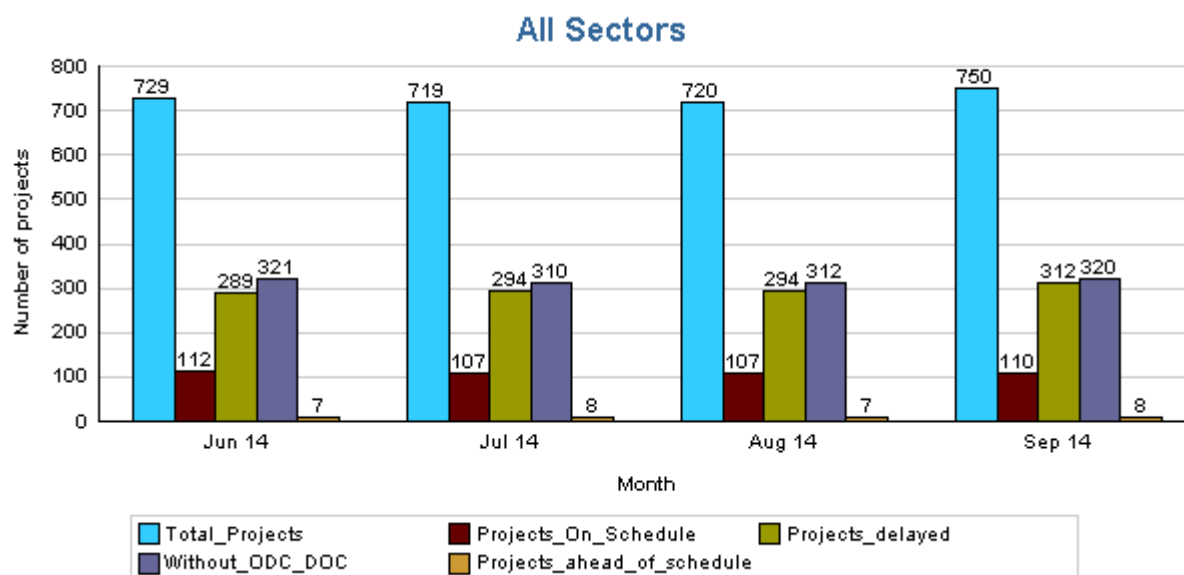

Break-up of 312 Delayed projects in September 2014

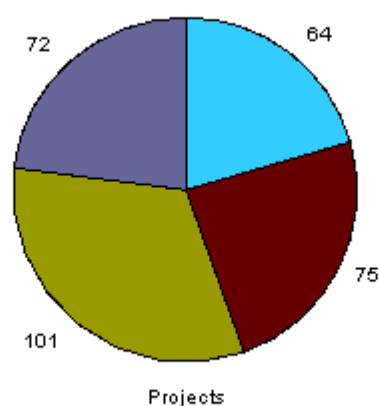


Delay in Months


Legend:

- 1-12
- 13-24
- 25-60
- MORE THAN 60

Graphical Presentation of URBAN DEVELOPMENT Sector

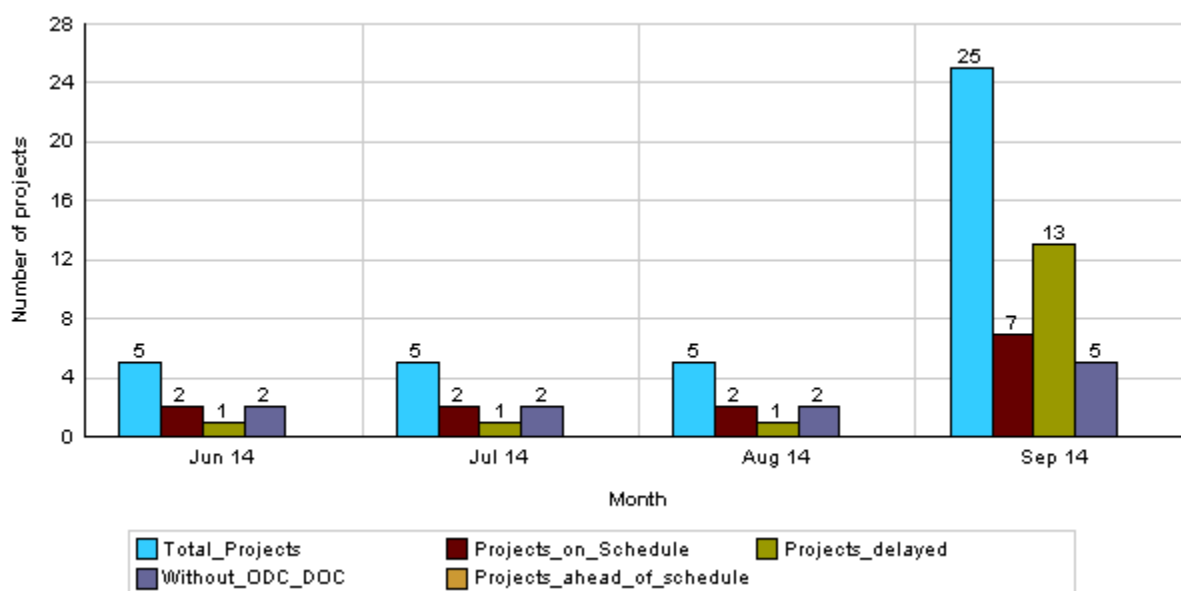


Break-up of 13 Delayed projects in September 2014

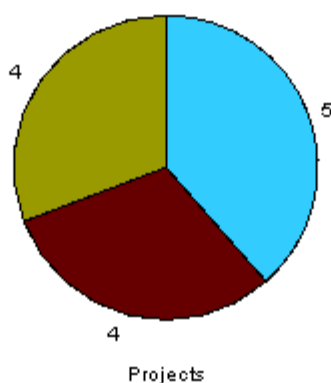


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Projects	5	4	4	0

Graphical Presentation of TELECOMMUNICATIONS Sector

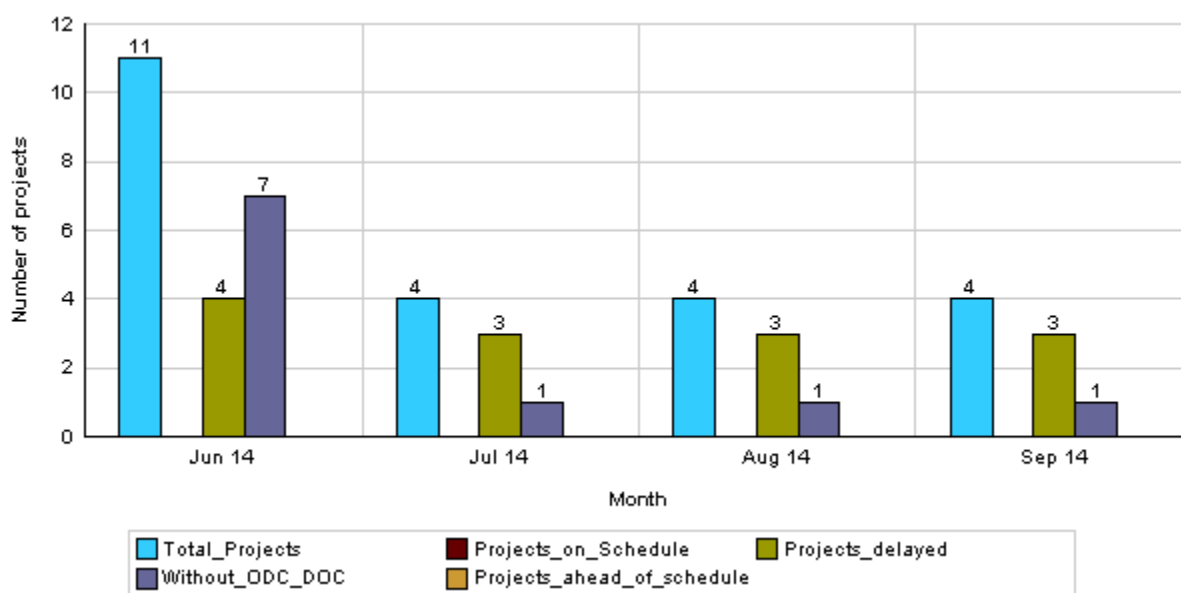


Break-up of 3 Delayed projects in September 2014

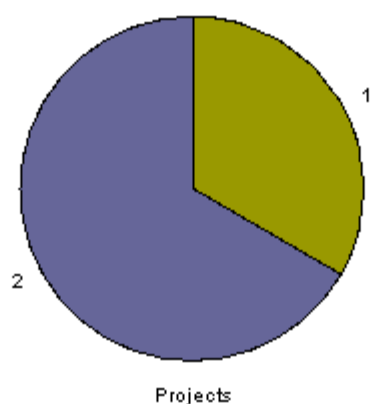


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	0	0	1	2

Graphical Presentation of SHIPPING AND PORTS Sector

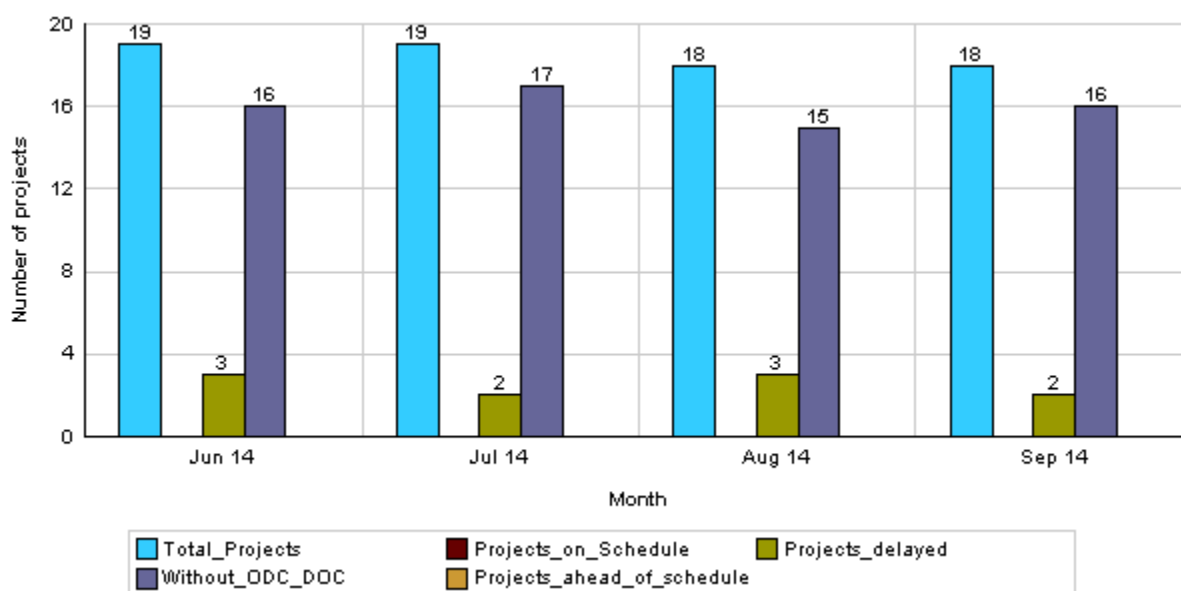


Break-up of 2 Delayed projects in September 2014

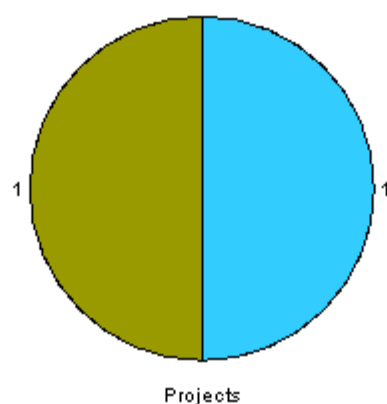


Delay in Months

Legend: 1-12 (Light Blue), 13-24 (Dark Red), 25-60 (Olive Green), MORE THAN 60 (Dark Blue)

Graphical Presentation of ROAD TRANSPORT AND HIGHWAYS Sector

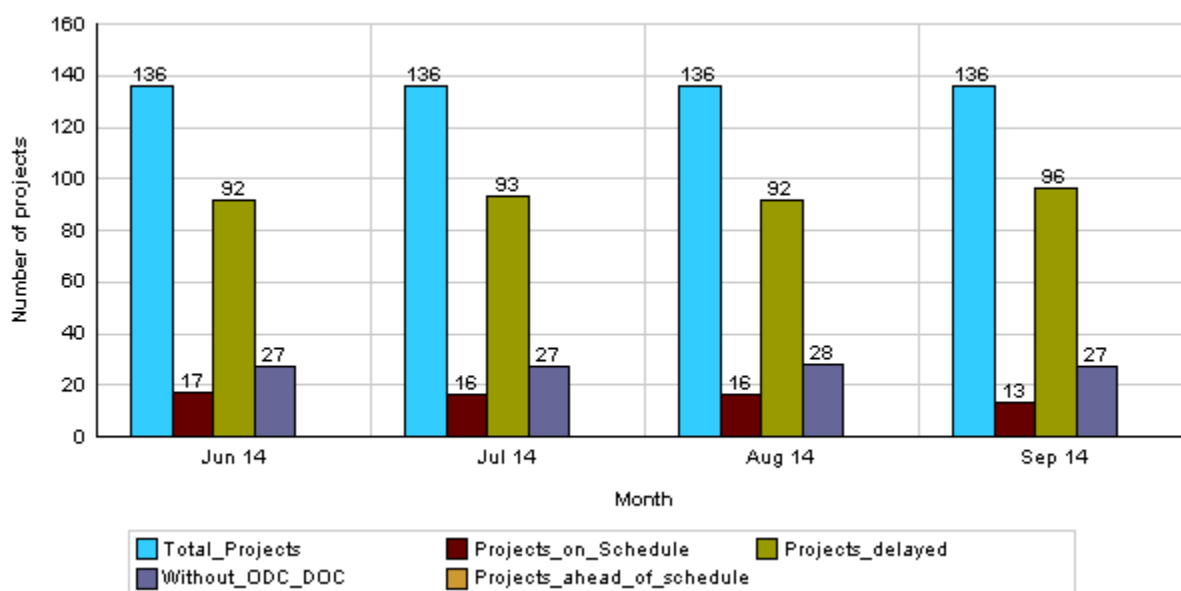


Break-up of 96 Delayed projects in September 2014

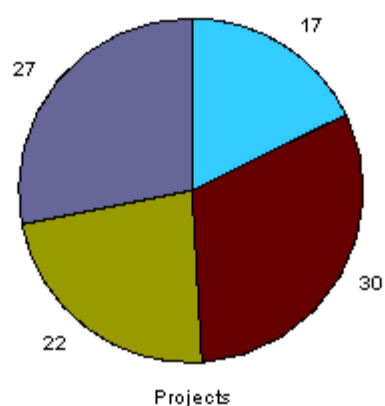


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Projects	17	30	22	27

Graphical Presentation of RAILWAYS Sector

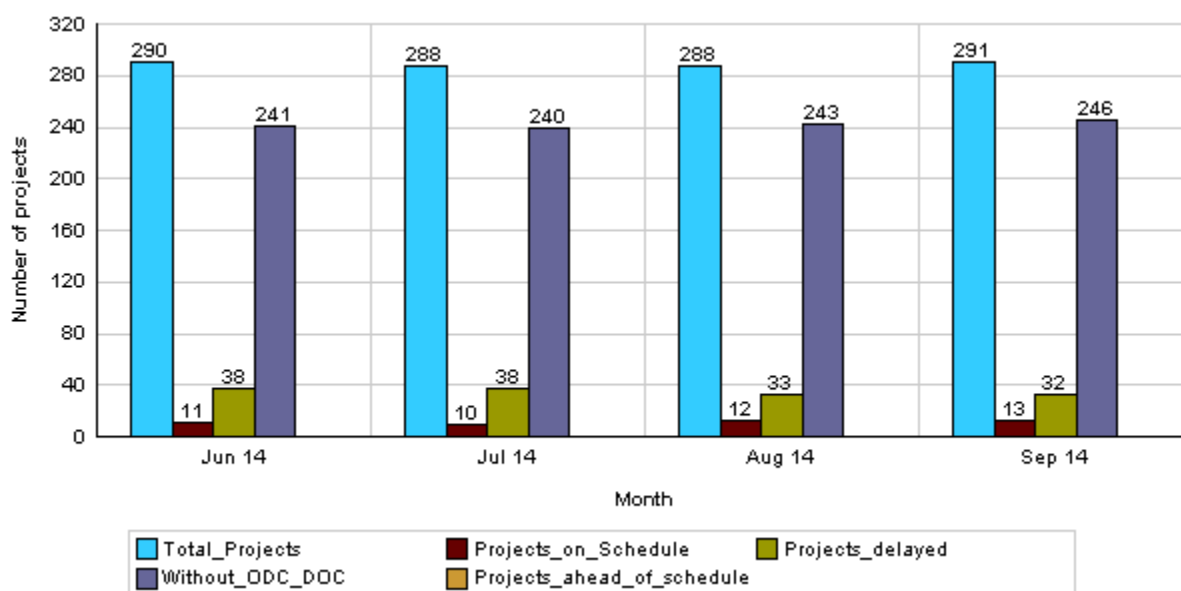


Break-up of 32 Delayed projects in September 2014

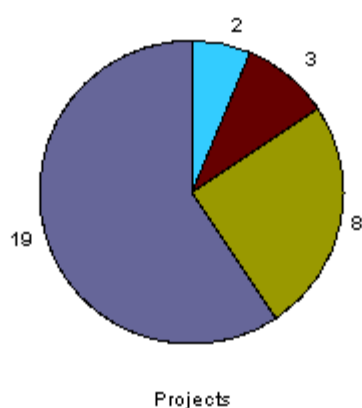


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	2	3	8	19

Graphical Presentation of POWER Sector

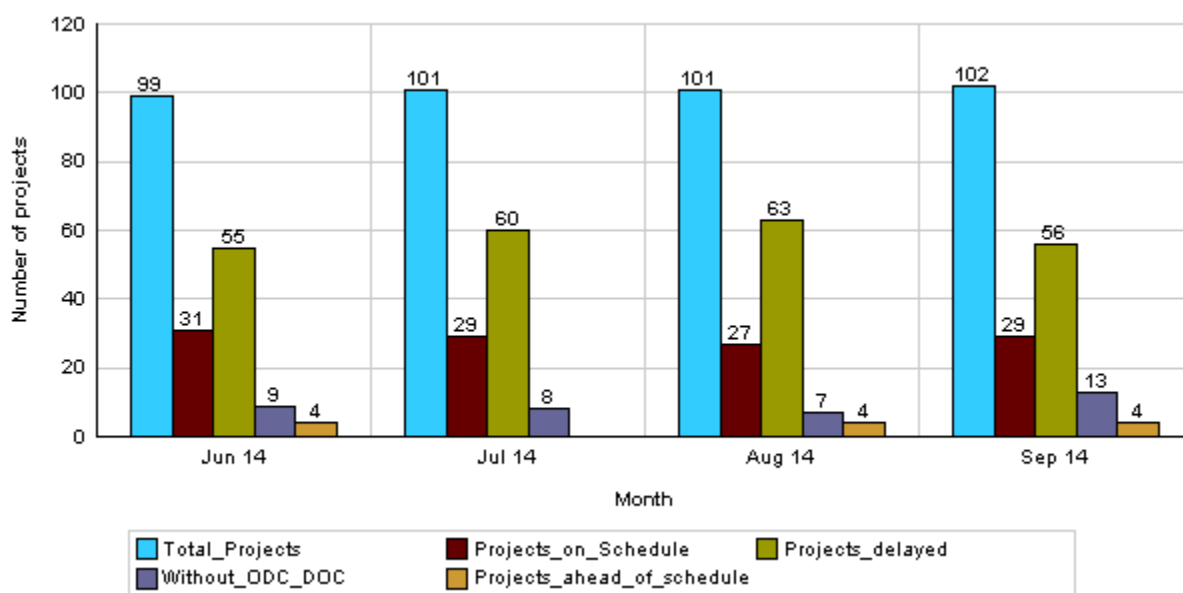


Break-up of 56 Delayed projects in September 2014

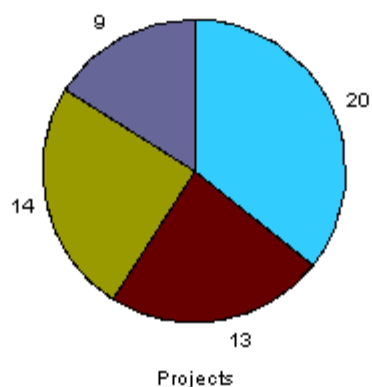


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	20			
13-24		13		
25-60			14	
MORE THAN 60				9

Graphical Presentation of PETROLEUM Sector

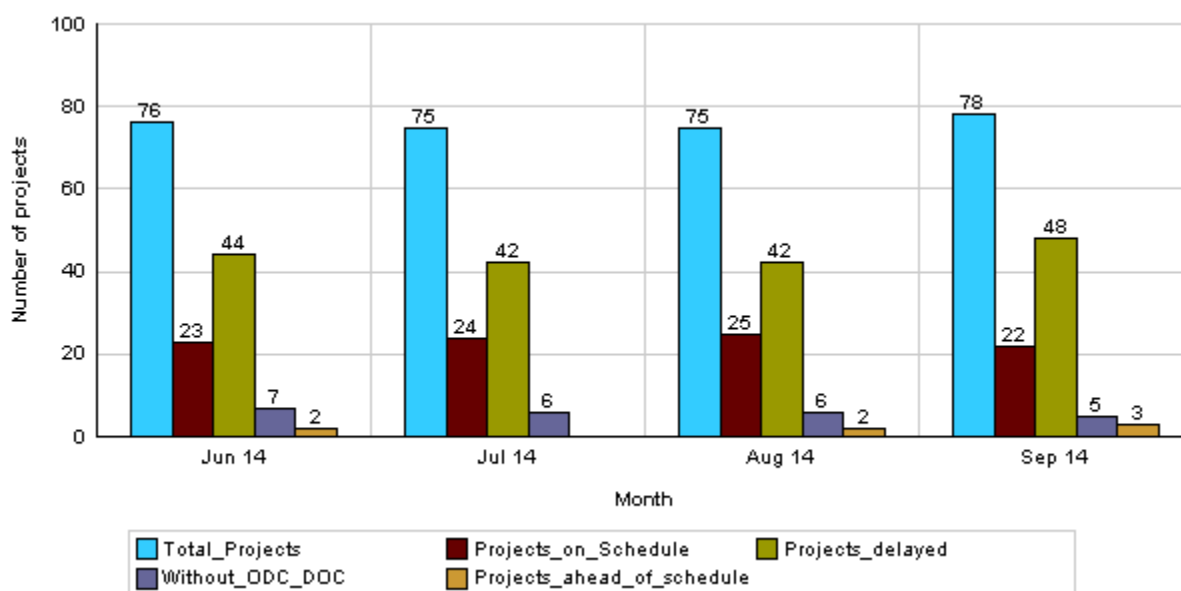


Break-up of 48 Delayed projects in September 2014

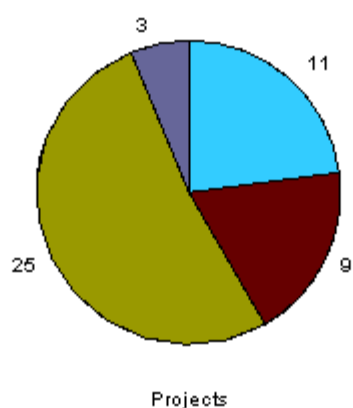


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
-----------------	------	-------	-------	--------------

Graphical Presentation of STEEL Sector

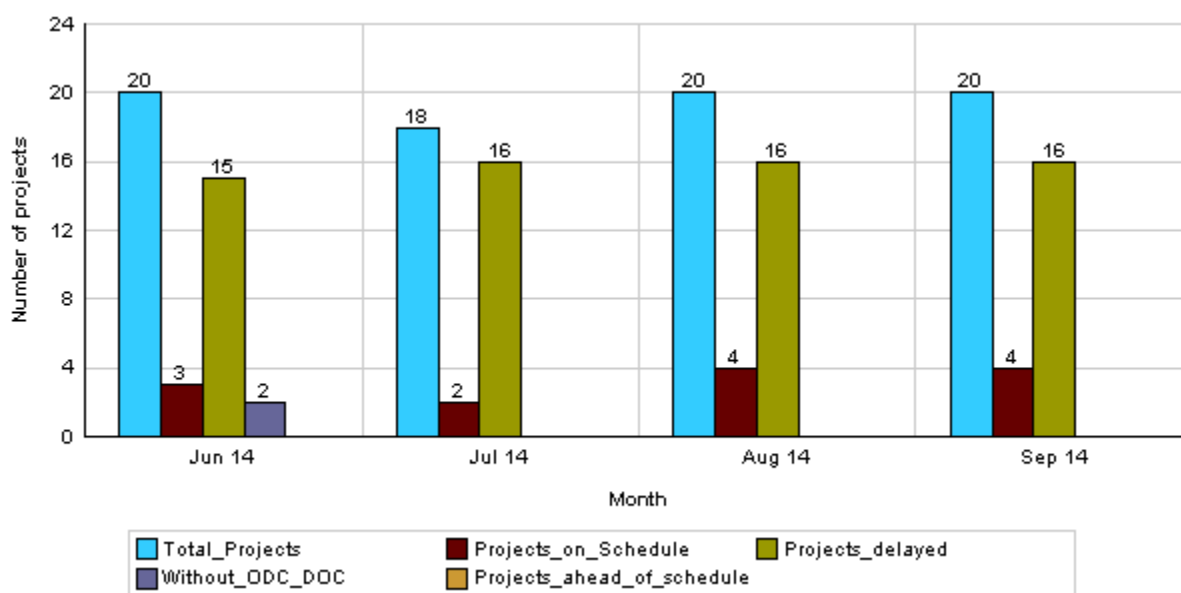


Break-up of 16 Delayed projects in September 2014

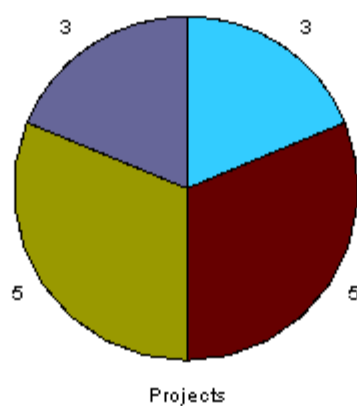


Delay in Months: 1-12 13-24 25-60 MORE THAN 60

Graphical Presentation of COAL Sector

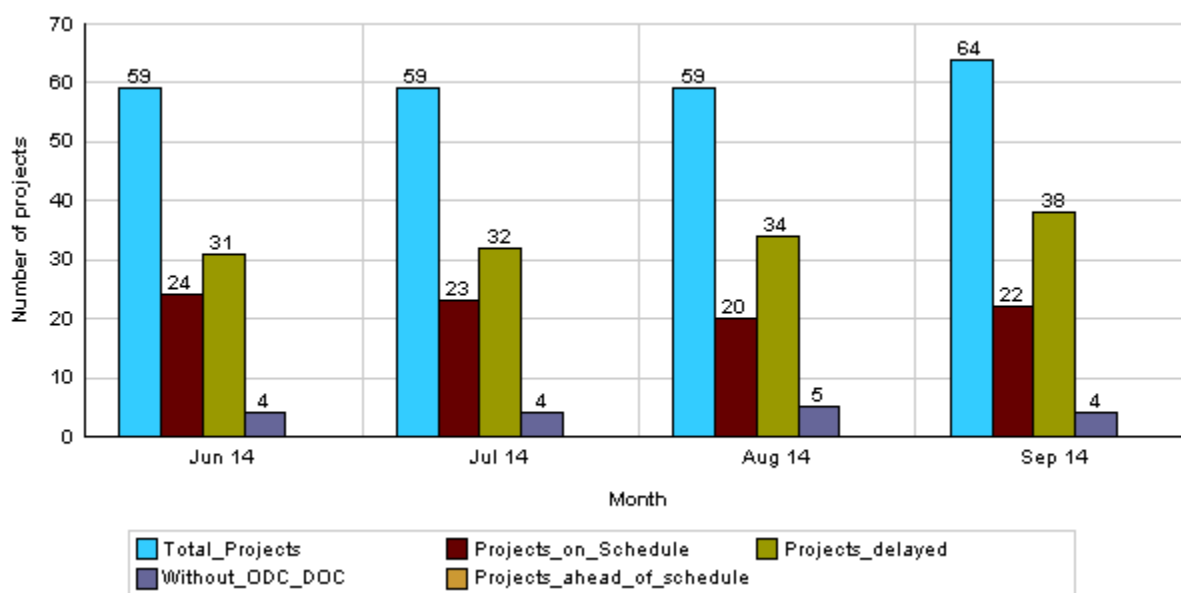


Break-up of 38 Delayed projects in September 2014

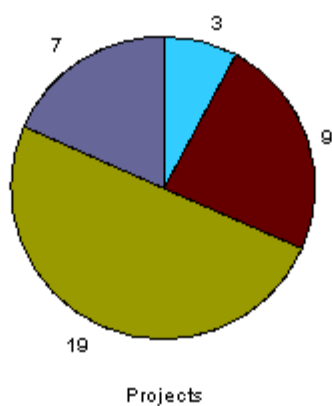


Delay in Months: 1-12, 13-24, 25-60, MORE THAN 60

Graphical Presentation of CIVIL AVIATION Sector

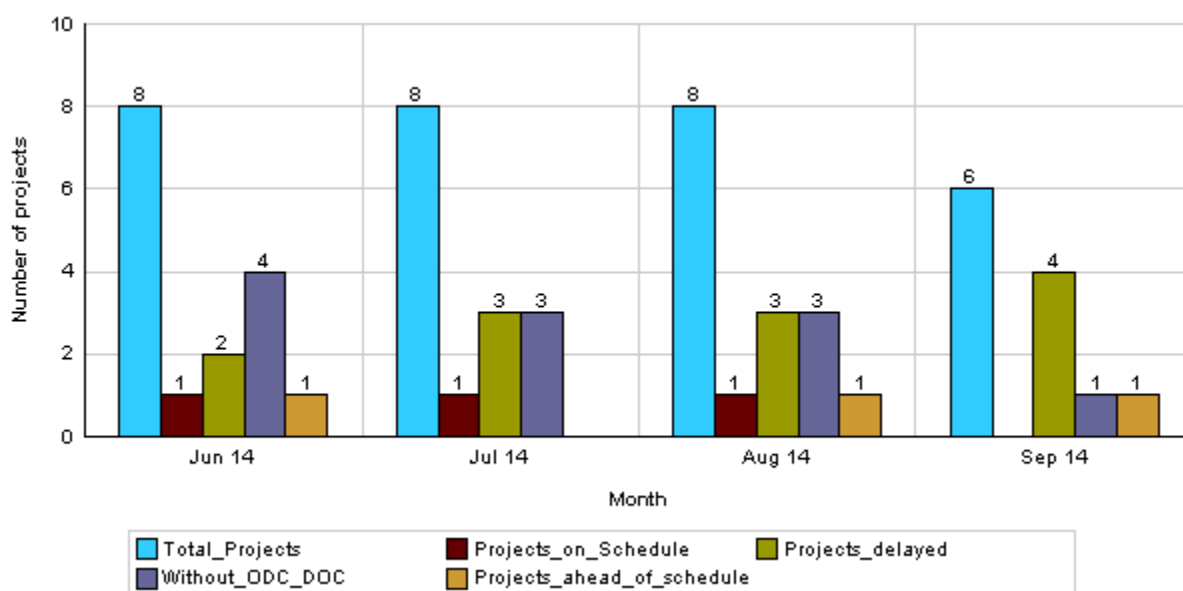


Break-up of 4 Delayed projects in September 2014

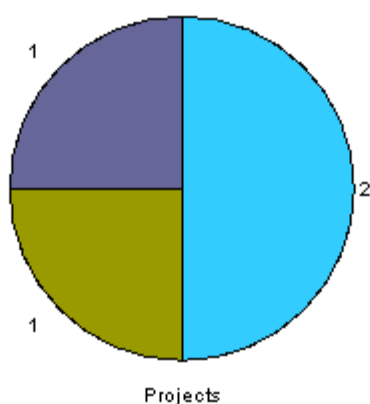


Delay in Months

1-12	13-24	25-60	MORE THAN 60
2	0	1	1

Graphical Presentation of ATOMIC ENERGY Sector

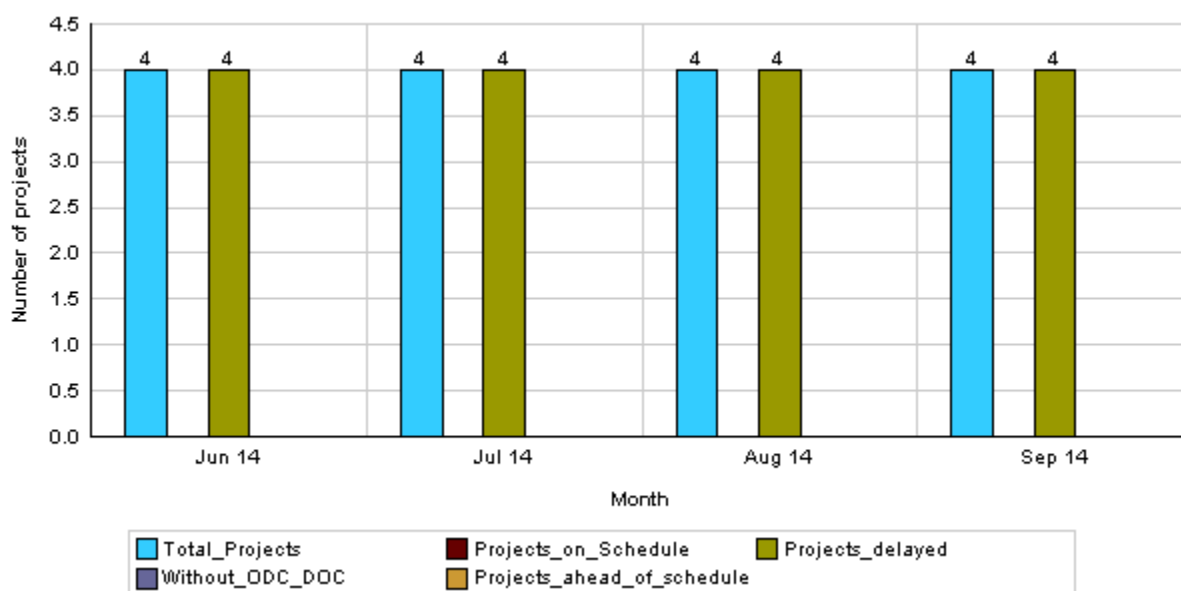

Break-up of 4 Delayed projects in September 2014

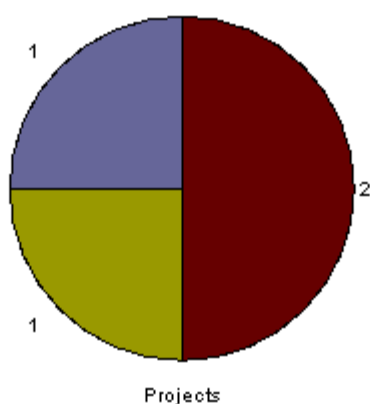

Delay in Months: 1-12 (Blue), 13-24 (Dark Red), 25-60 (Olive Green), MORE THAN 60 (Purple)

Sectorwise analysis of projects					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	40,442.00	46,726.00	46,726.00	31,310.19
CIVIL AVIATION	6	2,284.95	2,284.95	2,337.87	1,383.53
COAL	64	46,558.77	51,201.03	56,675.18	19,996.96
STEEL	20	66,395.10	70,414.06	72,349.06	61,760.12
PETROCHEMICALS	1	5,460.61	5,460.61	8,920.00	7,924.14
PETROLEUM	78	178,906.90	197,614.03	195,033.69	78,840.32
POWER	102	244,305.12	245,180.57	259,040.96	118,701.27
RAILWAYS	291	163,873.51	177,101.73	274,821.46	87,781.12
ROAD TRANSPORT AND HIGHWAYS	136	102,321.44	102,692.45	104,388.44	95,853.02
SHIPPING AND PORTS	18	12,117.12	13,337.95	14,390.98	4,748.99
TELECOMMUNICATIONS	4	2,018.15	2,018.15	1,843.90	582.21
URBAN DEVELOPMENT	25	82,686.31	82,745.21	87,959.21	14,916.15
WATER RESOURCES	1	542.90	542.90	1,187.00	35.49
Grand total	750	947,912.88	997,319.64	1,125,673.75	523,833.51

(All Cost/ Expenditure in Rs. Crore)

Sector Wise Details

(September 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	5,399.00	12/2015 11/2016	10/2017	22(O) 11(R)	4/70
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00 17,270.00	17,270.00	17,894.00	12/2008 10/2013	11/2014	71(O) 13(R)	40/102
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 5,677.00	5,677.00	4,723.19	09/2010 03/2015	03/2015	54(O) 0(R)	12/88
4	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	3,294.00	12/2016 03/2017	05/2018	17(O) 14(R)	4/69
	Total		40,442.00 -	46,726.00	31,310.19				60/329
	<u>CIVIL AVIATION</u>								
5	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	309.46	277.91	01/2011 04/2013	12/2016	71(O) 44(R)	0/0
6	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 335.61	388.53	284.00	05/2012 -	10/2014	29(O) -	0/0
7	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]AAI,CHANDIGARH	02/2011	452.00 -	452.00	309.21	03/2015 -	02/2015	-1(O) -	0/0
8	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	344.28	19.61	03/2014 -	01/2015	10(O) -	0/0
9	GAGAN PROJECT - [N04000065]AAI,MULTI STATE	09/2008	626.00 -	626.00	492.76	06/2013 -	06/2013	-	0/0
10	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	217.60	0.04	03/2015 -	03/2016	12(O) -	0/0
	Total		2,284.95 -	2,337.87	1,383.53				0/0
	<u>COAL</u>								
11	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,TELANGANA	12/2009	212.34 1,228.39	1,228.39	1,228.77	03/2013 09/2012	09/2015	30(O) 36(R)	21/22
12	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH	11/2009	150.59 -	198.59	94.90	03/2016 -	03/2016	0(O) -	2/7
13	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]NCL,MADHYA PRADESH	12/2009	1,352.04 1,143.54	1,143.54	664.83	03/2016 03/2016	03/2016	0(O) 0(R)	0/4
14	AMRAPALI OC(12MTY) - [N06000103]CCL,JHARKHAND	02/2012	858.11 -	858.11	97.05	03/2020 -	03/2020	0(O) -	0/3
15	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	170.25	03/2012 -	03/2017	60(O) -	4/5
16	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	471.66 341.63	341.63	102.07	03/2011 -	03/2017	72(O) -	0/2

Sector Wise Details

(September 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
17	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	146.04	03/2010 -	03/2017	84(O) -	3/4
18	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56 -	258.56	60.25	03/2016 -	03/2016	0(O) -	0/6
19	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA	05/2014	479.15 -	479.15	-	03/2019 -	03/2019	0(O) -	0/0
20	BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH	09/2008	203.82 -	203.82	-	03/2015 -	03/2015	0(O) -	1/6
21	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.00 -	490.10	183.63	03/2017 -	03/2017	0(O) -	3/11
22	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL,CHHATISGARH	05/2014	164.49 -	164.49	22.10	03/2020 -	03/2020	0(O) -	0/0
23	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,MADHYA PRADESH	06/2011	746.04 -	535.10	273.52	03/2015 -	03/2015	0(O) -	0/3
24	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH	12/2013	610.33 -	610.33	-	03/2022 -	03/2022	0(O) -	0/7
25	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35 -	462.35	273.00	03/2014 -	03/2016	24(O) -	2/9
26	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	35.52	03/2011 -	03/2016	60(O) -	0/2
27	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,560.52	03/2014 -	03/2016	24(O) -	6/13
28	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,583.65	03/2014 -	03/2016	24(O) -	10/16
29	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,ODISHA	02/2008	395.87 -	395.87	76.74	03/2015 -	03/2021	72(O) -	1/12
30	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.63 -	479.63	118.51	03/2013 -	03/2017	48(O) -	2/7
31	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA	05/2014	337.66 -	337.66	-	03/2019 -	03/2019	0(O) -	0/0
32	JAGANNATHPOR OC - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	152.43	21.55	03/2015 -	03/2017	24(O) -	1/7
33	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	447.06	29.03	03/2015 -	03/2018	36(O) -	4/31
34	JALLARAM SHAFT PROJECT - [N06000025]SCCL,TELANGANA	09/2007	467.78 -	467.78	2.85	03/2013 -	-	-	6/83
35	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL	11/2006	287.18 -	287.17	44.71	03/2011 -	03/2017	72(O) -	0/1
36	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	453.63	105.42	12/2012 -	03/2015	27(O) -	11/44
37	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	417.33	2.22	07/2016 -	03/2017	8(O) -	3/39
38	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	120.75	03/2013 -	03/2017	48(O) -	3/9
39	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND	08/2011	988.35 -	988.35	6.84	04/2017 -	04/2017	0(O) -	0/0
40	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	55.96	03/2014 -	03/2017	36(O) -	0/2
41	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24(O) -	1/7

Sector Wise Details

(September 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
42	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]NCL,UTTAR PRADESH	06/2011	1,131.28 -	1,131.28	43.25	03/2018 -	03/2018	0(O) -	0/4
43	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	242.29	0.30	03/2015 -	03/2018	36(O) -	0/28
44	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,UTTAR PRADESH	06/2011	789.88 -	741.62	404.39	03/2013 -	03/2014	-	0/2
45	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA	06/2014	289.03 -	289.03	-	03/2018 -	03/2018	0(O) -	0/0
46	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	129.48	03/2010 -	03/2017	84(O) -	8/10
47	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH	06/2008	1,188.31 -	7,612.33	755.52	03/2013 -	03/2023	120(O) -	0/16
48	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	469.78 -	706.40	44.65	07/2012 -	03/2016	44(O) -	0/3
49	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.42 -	321.50	211.59	03/2014 -	03/2016	24(O) -	1/6
50	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	181.19	36.13	03/2012 -	03/2016	48(O) -	4/6
51	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 2,500.00	1,230.27	1,000.00	04/2015 12/2018	04/2019	48(O) 4(R)	0/0
52	MURAI DIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	-	04/2014 -	04/2014	-	0/0
53	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 -	5,907.11	371.49	12/2015 -	04/2018	28(O) -	9/35
54	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 -	259.40	7.45	03/2012 -	03/2015	36(O) -	0/2
55	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND	02/2014	555.52 -	555.52	6.84	03/2021 -	03/2021	0(O) -	0/0
56	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	60.93	03/2012 -	03/2017	60(O) -	0/2
57	PELMA OCP(10.00MTY) - [N06000045]SECL,CHHATISGARH	07/2008	448.32 -	448.32	0.46	03/2015 -	03/2015	0(O) -	1/1
58	PENGANGA OC - [N06000066]WCL,MAHARASHTRA	10/2008	339.77 -	339.77	1.69	03/2014 -	03/2016	24(O) -	0/1
59	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	144.07	03/2013 -	03/2015	24(O) -	1/3
60	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	42.46	03/2014 -	03/2016	24(O) -	0/0
61	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	223.57	03/2016 -	03/2016	0(O) -	0/2
62	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	418.97	229.11	03/2012 -	03/2016	48(O) -	24/27
63	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	162.76	2.48	03/2015 -	03/2015	0(O) -	4/29
64	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.14 -	430.14	68.08	03/2016 -	03/2016	0(O) -	6/48
65	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	6.56	06/2015 -	06/2016	12(O) -	3/51
66	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78 -	209.78	68.51	03/2015 -	03/2015	0(O) -	8/31

Sector Wise Details

(September 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
67	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	249.03	72.38	03/2012 -	-	-	24/42
68	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA	05/2014	3,756.36 -	3,756.36	-	03/2026 -	03/2026	0(O) -	0/0
69	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05 -	1,055.05	30.31	03/2018 -	03/2018	0(O) -	0/0
70	TALABIRA OCP - [N06000043]MCL,ODISHA	03/2008	447.72 -	447.72	52.34	03/2016 -	03/2020	48(O) -	0/11
71	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	142.19	03/2012 -	03/2016	48(O) -	0/2
72	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,TAMIL NADU	10/2004	2,030.78 3,027.59	3,321.86	3,035.56	06/2009 03/2013	10/2014	64(O) 19(R)	19/23
73	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	5,632.17	03/2012 05/2014	11/2014	32(O) 6(R)	25/39
74	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]NLC,TAMIL NADU	04/2012	364.75 -	364.75	92.32	10/2014 -	11/2014	1(O) -	3/11
	Total		46,558.77 -	56,675.18	19,996.96				224/797
	<u>STEEL</u>								
75	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,KARNATAKA	04/2011	572.00 -	572.00	404.31	04/2013 09/2014	03/2015	23(O) 6(R)	17/18
76	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND	10/2013	245.67 -	245.67	18.01	05/2016 -	05/2016	0(O) -	0/3
77	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,KARNATAKA	02/2011	898.55 -	898.55	343.43	05/2013 01/2015	03/2015	22(O) 2(R)	14/20
78	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]RINL,MULTI STATE	07/2007	480.00 -	450.00	322.07	09/2009 05/2012	03/2015	66(O) 34(R)	1/1
79	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]NMDC,CHHATISGARH	01/2007	295.89 607.17	607.17	376.30	12/2011 01/2015	03/2015	39(O) 2(R)	16/20
80	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,ANDHRA PRADESH	06/2006	108.00 216.68	216.68	164.85	09/2008 12/2013	10/2014	73(O) 10(R)	3/4
81	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHHATISGARH - [N12000078]SAIL,CHHATISGARH	07/2012	332.65 -	332.65	137.76	08/2014 -	01/2015	5(O) -	3/4
82	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH	04/2014	188.93 -	188.93	-	04/2015 -	04/2015	0(O) -	0/3
83	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL,ODISHA	11/2011	254.55 -	254.55	114.35	11/2013 -	06/2015	19(O) -	2/4
84	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	13,392.35	03/2013 -	09/2015	30(O) -	30/35
85	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,JHARKHAND	05/2010	6,325.00 -	6,325.00	4,856.37	12/2011 -	12/2014	36(O) -	19/24
86	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,WEST BENGAL	08/2010	2,875.00 -	2,875.00	2,355.92	12/2012 -	03/2015	27(O) -	15/20
87	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,WEST BENGAL	06/2008	14,443.00 -	16,408.00	16,340.70	12/2011 -	12/2014	36(O) -	23/29
88	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL,ANDHRA PRADESH	10/2005	8,692.00 12,291.00	12,291.00	10,976.01	10/2009 10/2012	12/2014	62(O) 26(R)	68/68

Sector Wise Details

(September 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
89	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]SAIL, ODISHA	08/2010	11,812.00 -	11,812.00	11,497.14	03/2013 -	03/2015	24(O) -	18/20
90	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL, MAHARASHTRA	12/2011	187.33 -	187.33	138.60	10/2013 -	08/2015	22(O) -	2/5
91	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL, ODISHA	10/2012	160.48 -	160.48	97.05	09/2014 -	01/2015	4(O) -	0/2
92	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]SAIL, WEST BENGAL	11/2012	313.05 -	313.05	135.24	06/2015 -	06/2015	0(O) -	2/3
93	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079]SAIL, ODISHA	06/2012	237.09 -	237.09	87.87	12/2014 -	03/2015	3(O) -	0/2
94	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]SAIL, ODISHA	06/2014	708.91 -	708.91	1.79	04/2016 -	04/2016	0(O) -	0/2
	Total		66,395.10 -	72,349.06	61,760.12				233/287
	<u>PETROCHEMICALS</u>								
95	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, ASSAM	04/2006	5,460.61 -	8,920.00	7,924.14	04/2012 -	-	-	22/29
	Total		5,460.61 -	8,920.00	7,924.14				22/29
	<u>PETROLEUM</u>								
96	102 MW WIND POWER PROJECT - [N16000119]ONGC, RAJASTHAN	07/2010	1,106.00 -	678.02	405.00	06/2012 -	12/2014	30(O) -	0/3
97	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]ONGC, MULTI STATE	03/2014	2,476.82 -	2,476.82	-	12/2018 -	12/2018	0(O) -	0/0
98	AHMEDABAD REDEVELOPMENT PROJECT - [N16000120]ONGC, GUJARAT	11/2010	1,916.10 -	1,916.10	1,160.14	12/2014 -	12/2017	36(O) -	0/0
99	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC, GUJARAT	11/2010	2,189.63 -	2,189.63	1,039.42	12/2014 -	12/2018	48(O) -	0/0
100	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, ASSAM	03/2009	2,465.15 -	2,378.86	1,711.73	03/2013 03/2015	03/2016	36(O) 12(R)	0/5
101	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL, MULTI STATE	08/2011	586.00 -	586.00	198.47	08/2015 -	08/2015	0(O) -	0/12
102	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL, ASSAM	08/2008	144.02 204.29	204.29	155.04	06/2012 09/2013	12/2014	30(O) 15(R)	0/0
103	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS (OSV) - [N16000084]ONGC, MULTI STATE	06/2007	736.65 -	736.65	469.52	09/2011 -	12/2015	51(O) -	0/0
104	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC, MULTI STATE	11/2010	331.20 -	269.10	190.04	08/2013 -	05/2015	21(O) -	0/5
105	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC, GUJARAT	03/2009	302.26 -	240.95	106.67	09/2012 -	03/2015	30(O) -	0/0
106	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC, MULTI STATE	01/2010	723.64 -	723.64	-	03/2013 -	06/2016	39(O) -	0/0
107	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT (MOPS) - [N16000128]ONGC, MAHARASHTRA	03/2011	861.79 -	761.68	634.95	05/2013 06/2014	03/2015	22(O) 9(R)	0/5

Sector Wise Details

(September 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
108	DABHOL BANGALORE PIPELINE PROJECT PHASE-II - [N16000147]GAIL,MULTI STATE	06/2009	486.00 -	486.00	107.14	09/2013 -	02/2015	17(O) -	0/1
109	DBNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,MULTI STATE	12/2009	540.92 -	540.92	340.92	06/2011 07/2012	-	-	6/7
110	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA	12/2009	1,584.00 -	1,584.00	1,006.92	- -	08/2015	- -	0/12
111	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,MULTI STATE	04/2003	429.82 3,955.21	3,955.21	3,413.13	04/2006 04/2016	06/2015	110(O) -10(R)	0/0
112	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,MAHARASHTRA	06/2007	3,248.78 5,633.44	6,000.00	5,867.78	08/2010 03/2012	05/2015	57(O) 38(R)	0/10
113	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 -	2,592.17	310.34	05/2014 -	05/2015	12(O) -	0/9
114	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]ONGC,MULTI STATE	03/2010	3,241.03 6,638.94	6,638.94	2,192.69	03/2013 11/2014	11/2014	20(O) 0(R)	0/10
115	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC,MULTI STATE	04/2013	284.82 -	284.82	-	04/2015 -	04/2015	0(O) -	0/0
116	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17 -	600.17	248.92	12/2014 -	05/2015	5(O) -	0/8
117	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE	06/2010	2,523.00 -	2,523.00	1,013.04	01/2014 -	12/2015	23(O) -	0/9
118	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]ONGC,MULTI STATE	10/2013	429.06 -	429.06	-	10/2014 -	12/2014	2(O) -	0/0
119	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,ANDHRA PRADESH	03/2009	3,597.00 2,730.00	2,730.00	3,128.58	09/2011 03/2012	11/2014	38(O) 32(R)	56/59
120	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL, WEST BENGAL	03/2014	3,076.00 -	3,076.00	42.24	09/2017 -	09/2017	0(O) -	0/0
121	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL, TAMIL NADU	05/2013	711.00 -	711.00	3.37	- -	-	-	0/0
122	GAS TURBINE GENERATION SET - [N18000146]OIL, ASSAM	07/2009	216.88 -	216.88	186.44	10/2011 12/2014	12/2014	38(O) 0(R)	0/9
123	GUJARAT REGION PIPELINE REPLACEMENT PROJECT - [N16000189]GAIL, GUJARAT	07/2014	716.00 -	716.00	-	01/2017 -	01/2017	0(O) -	0/0
124	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]ONGC,MAHARASHTRA	03/2012	5,608.40 -	5,608.40	2,805.04	05/2015 -	05/2015	0(O) -	0/17
125	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]IOCL, ASSAM	02/2014	163.88 -	163.88	3.82	07/2016 -	07/2016	0(O) -	0/0
126	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	598.34	03/2015 -	05/2015	2(O) -	0/12
127	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]ONGC,MAHARASHTRA	12/2012	3,513.07 -	3,513.07	0.27	02/2016 -	02/2016	0(O) -	0/0
128	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE	05/2013	4,124.35 -	4,124.35	-	04/2016 -	04/2016	0(O) -	0/0
129	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL, KERALA	03/2012	14,225.00 16,504.00	16,504.00	3,483.53	05/2016 -	05/2016	0(O) -	0/0
130	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE	01/2012	352.49 -	352.49	99.82	03/2014 -	04/2015	13(O) -	0/5
131	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18 -	7,596.18	13.50	01/2013 -	02/2019	73(O) -	0/0

Sector Wise Details

(September 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
132	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,HARYANA	11/2007	281.07 -	281.07	6.84	10/2010 -	-	-	0/0
133	KG BASIN PIPELINE REPLACEMENT PROJECT - [N16000190]GAIL,ANDHRA PRADESH	07/2014	762.00 -	762.00	-	01/2017 -	01/2017	0(O) -	0/0
134	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00 -	2,300.00	1,408.97	12/2012 06/2015	06/2015	30(O) 0(R)	0/14
135	KOTA JOBNER PIPELINE PROJECT - [N16000170]BPCL,RAJASTHAN	04/2011	276.26 -	276.27	174.81	12/2015 -	03/2015	-9(O) -	0/64
136	LPG MARKETING TERMINAL, PARADIP - [N16000174]IOCL,ODISHA	07/2009	158.91 -	158.91	113.85	03/2015 -	02/2015	-1(O) -	0/0
137	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	12/2012	607.06 -	607.06	47.38	01/2016 -	01/2016	0(O) -	0/0
138	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,KARNATAKA	02/2012	666.00 701.00	701.00	312.24	11/2015 -	11/2015	0(O) -	22/29
139	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL,ODISHA	07/2009	199.75 -	199.75	145.55	07/2013 -	12/2014	17(O) -	0/0
140	MEHESANA REDEVELOPMENT PROJECT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	3,823.00	1,076.57	04/2015 -	12/2017	32(O) -	0/0
141	MH NORTH REDEVELOPMENT PHASE III - [N16000188]ONGC,MAHARASHTRA	06/2014	5,706.47 -	5,706.47	-	05/2017 -	05/2017	0(O) -	0/0
142	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL,TAMIL NADU	12/2012	279.00 -	279.00	95.32	12/2014 -	12/2014	0(O) -	0/57
143	MRPL PHASE-III EXPANSION - [N16000114]MANGALORE REFIN,KARNATAKA	08/2008	12,412.00 -	12,160.26	-	01/2012 -	09/2014	32(O) -	0/108
144	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	171.83	-	-	-	-	0/0
145	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	913.00	326.01	07/2015 -	12/2015	5(O) -	0/0
146	PARADIP REFINERY PROJECT - [N16000058]IOCL,ODISHA	02/2009	29,777.00 34,555.00	34,555.00	26,919.64	11/2012 11/2013	03/2015	28(O) 16(R)	74/100
147	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	1,019.33	09/2012 -	12/2015	39(O) -	6/7
148	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,MULTI STATE	08/2010	8,140.00 -	8,140.00	7,117.42	02/2014 -	03/2015	13(O) -	0/0
149	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]BPCL,MAHARASHTRA	08/2009	246.81 276.83	276.83	261.43	08/2012 -	10/2014	26(O) -	0/0
150	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT	09/2011	202.25 -	160.16	36.33	07/2016 -	07/2016	0(O) -	0/5
151	PIPELINE REPLACEMENT PROJECT-3 - [N16000137]ONGC,MULTI STATE	04/2012	2,547.26 -	1,417.00	1,304.57	05/2014 -	05/2015	12(O) -	0/5
152	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	3,150.00	92.49	09/2017 -	09/2017	0(O) -	0/0
153	POLYPROPYLENE UNIT - [N16000113]MANGALORE REFIN,KARNATAKA	05/2009	1,803.78 -	1,803.78	1,016.69	07/2012 -	10/2014	27(O) -	0/31
154	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	270.00	-	12/2014 03/2016	03/2016	15(O) 0(R)	0/0
155	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 -	1,138.50	145.86	04/2015 -	04/2015	0(O) -	0/0
156	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL,MAHARASHTRA	03/2012	1,419.00 -	1,419.00	771.67	12/2014 -	03/2015	3(O) -	0/1

Sector Wise Details

(September 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
157	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]IOCL,BIHAR	04/2013	480.00 -	480.00	3.02	02/2016 -	02/2016	0(O) -	0/0
158	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU	02/2011	3,110.36 -	3,110.36	242.84	11/2015 -	11/2015	0(O) -	0/52
159	RESITEMENT OF BILASPUR AND BISRAMPUR DEPOTS TO KORBA (CHATTISGARH) - [N16000186]IOCL,CHHATISGARH	01/2011	141.86 219.08	219.08	93.99	09/2016 -	12/2015	-9(O) -	0/12
160	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96 -	191.96	53.98	05/2015 -	12/2015	7(O) -	0/12
161	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS - [N16000181]ONGC,MULTI STATE	03/2013	2,913.10 -	2,910.30	9.50	05/2016 -	05/2016	0(O) -	0/0
162	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL,GUJARAT	12/2011	160.00 -	160.00	-	03/2014 -	07/2016	28(O) -	0/0
163	REWARI KANPUR PIPELINE PROJECT - [N16000145]HPCL,MULTI STATE	02/2012	1,210.64 -	1,210.64	732.58	11/2015 -	11/2015	0(O) -	14/25
164	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	08/2006	94.00 352.56	352.56	10.60	09/2012 03/2017	03/2017	54(O) 0(R)	0/0
165	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	888.80	10/2011 -	10/2015	48(O) -	0/0
166	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,283.65	01/2012 -	10/2015	45(O) -	0/0
167	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,ANDHRA PRADESH	01/2006	672.00 1,038.00	1,038.00	991.73	10/2011 -	12/2014	38(O) -	0/0
168	SURAT PARADIP PIPELINE PROJECT - [N16000163]GAIL,MULTI STATE	10/2012	10,281.00 -	10,281.00	1.36	04/2015 -	12/2020	68(O) -	0/0
169	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]ONGC,TRIPURA	07/2008	288.04 288.04	253.66	216.68	08/2012 -	03/2015	31(O) -	0/5
170	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 1,200.00	1,200.00	55.28	03/2015 11/2015	11/2015	8(O) 0(R)	0/5
171	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 462.79	462.79	94.94	10/2014 -	10/2015	12(O) -	0/0
172	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	330.47	270.86	06/2011 03/2012	07/2015	49(O) 40(R)	13/20
173	WAX PROJECT - [N16000101]NRL,ASSAM	06/2010	576.60 676.05	676.05	560.73	12/2013 05/2014	10/2014	10(O) 5(R)	67/69
	Total		178,906.90 -	195,033.69	78,840.32				258/819
	<u>POWER</u>								
174	765 KV POOLING STATION AND NETWORK WITH DVC AND MAITHOB RBC - [N18000069]PGCIL,MULTI STATE	08/2008	7,075.33 -	7,075.33	-	08/2012 -	-	-	2/11
175	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]NEEPCO,TRIPURA	07/2012	296.87 -	296.87	279.18	- 03/2015	03/2015	- 0(R)	5/17
176	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 -	155.57	-	03/2016 -	03/2016	0(O) -	0/0

Sector Wise Details

(September 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
177	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]PGCIL,MULTI STATE	12/2012	156.04 -	156.04	-	10/2014 -	10/2014	0(O) -	2/7
178	BARH STPP STAGE -II - [N18000047]NTPC,BIHAR	02/2008	7,341.04 -	7,341.04	7,902.00	08/2013 -	03/2015	19(O) -	15/20
179	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	12/2003	8,692.97 -	8,693.00	10,264.00	12/2009 -	03/2017	87(O) -	23/46
180	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	6,749.18 - 6,749.18	6,749.18	4,726.00	07/2011 -	08/2016	61(O) -	8/34
181	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	237.85	12/2015 -	12/2015	0(O) -	2/19
182	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,479.66	09/2014 -	03/2015	6(O) -	6/19
183	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	598.63	06/2015 -	06/2015	0(O) -	0/0
184	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNAM OF ANDHRA PRADESH(PGCIL) - [N18000111]PGCIL,MULTI STATE	08/2011	1,637.34 -	1,637.34	-	08/2014 -	-	-	8/19
185	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,ANDHRA PRADESH	03/2012	206.44 -	206.44	43.97	06/2014 -	-	-	0/20
186	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	-	06/2015 -	06/2015	0(O) -	3/7
187	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139]PGCIL,TAMIL NADU	01/2013	182.80 -	182.80	76.33	10/2014 -	10/2014	0(O) -	2/14
188	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 -	196.58	-	02/2016 -	02/2016	0(O) -	0/7
189	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	892.43	11/2012 -	12/2015	37(O) -	1/12
190	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	1,364.52	-	05/2016 -	04/2016	-1(O) -	1/20
191	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 -	522.29	-	11/2016 -	11/2016	0(O) -	0/0
192	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	-	09/2014 -	09/2014	0(O) -	0/0
193	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATTISGARH	05/2011	1,961.87 -	1,961.87	1,528.65	05/2014 -	03/2015	10(O) -	2/11
194	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	02/2013	11,638.55 -	11,638.55	1,471.00	09/2017 -	03/2018	6(O) -	13/39
195	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,BIHAR	12/2011	901.77 -	901.77	-	08/2014 -	-	-	3/15
196	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]PGCIL,MULTI STATE	05/2014	303.07 -	303.07	-	07/2016 -	07/2016	0(O) -	0/0

Sector Wise Details

(September 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
197	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000107]PGCIL,CHHATISGARH	08/2011	1,391.97 -	1,391.97	-	12/2013 -	11/2014	11(O) -	4/8
198	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154]PGCIL,MAHARASHTRA	10/2013	1,315.90 -	1,315.90	-	11/2016 -	03/2016	-8(O) -	2/17
199	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,KARNATAKA	03/2005	1,007.16 -	1,007.16	946.81	12/2007 12/2009	-	-	1/10
200	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 -	4,653.95	3,241.37	12/2009 03/2017	03/2017	87(O) 0(R)	11/29
201	KISHANGANGA HEP - [N18000031]NHPC,JAMMU AND KASHMIR	07/2007	3,642.04 3,642.04	5,497.72	3,644.34	01/2016 -	11/2016	10(O) -	4/6
202	KOLDAM HEP (NTPC) - [180100211]NTPC,HIMACHAL PRADESH	10/2002	4,527.15 7,220.00	7,220.00	6,077.00	04/2009 -	05/2015	73(O) -	3/9
203	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	12/2011	15,166.19 -	15,166.19	5,031.00	12/2016 -	03/2018	15(O) -	19/23
204	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	2,159.07	1,880.15	09/2008 -	03/2013	-	14/23
205	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	11/2012	11,846.00 -	11,846.00	1,846.00	05/2017 -	03/2019	22(O) -	17/37
206	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	1,527.00	140.00	08/2017 -	03/2018	7(O) -	0/9
207	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	7,921.47	3,051.00	09/2016 -	03/2018	18(O) -	21/24
208	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	9,188.20	08/2013 -	06/2015	22(O) -	0/17
209	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL,MULTI STATE	02/2014	908.08 -	908.08	-	06/2016 -	06/2016	0(O) -	2/20
210	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 -	752.64	425.52	07/2013 -	03/2015	20(O) -	1/10
211	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	-	02/2012 -	-	-	0/13
212	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	415.06	11/2011 -	03/2016	52(O) -	1/13
213	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 -	539.82	-	06/2016 -	06/2016	0(O) -	4/20
214	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,086.62	04/2013 -	03/2016	35(O) -	0/11
215	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	412.62	11/2014 -	03/2015	4(O) -	2/16
216	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL,MULTI STATE	09/2013	680.69 -	680.69	-	03/2016 -	03/2016	0(O) -	1/17
217	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]PGCIL,MULTI STATE	09/2012	803.34 -	803.34	379.39	03/2015 -	03/2015	0(O) -	4/17
218	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	142.92	04/2015 -	05/2015	1(O) -	0/18
219	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	694.44	11/2012 -	03/2016	40(O) -	0/11

Sector Wise Details

(September 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
220	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]PGCIL,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	-	04/2020 -	04/2020	0(O) -	0/0
221	PARBATI HEP (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	5,366.00	4,667.37	09/2009 -	07/2018	106(O) -	6/12
222	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99 1,128.38	1,128.38	909.40	08/2013 -	09/2015	25(O) -	22/37
223	RAMPUR HEP(412 MW) - [N18000024]SJVN, HIMACHAL PRADESH	01/2007	2,047.03 -	2,047.03	-	03/2012 -	-	-	22/28
224	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 2,998.00	9,395.18	3,102.00	11/2016 -	03/2018	16(O) -	16/19
225	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE	05/2014	829.98 -	829.98	-	09/2016 -	09/2016	0(O) -	0/0
226	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]PGCIL,KARNATAKA	02/2014	167.40 -	167.40	-	12/2015 -	12/2015	0(O) -	1/7
227	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	6,285.33	6,943.84	09/2010 -	12/2018	99(O) -	0/0
228	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]PGCIL,MULTI STATE	08/2008	2,360.95 -	2,580.90	-	08/2012 -	09/2014	25(O) -	2/6
229	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,MULTI STATE	09/2012	1,508.74 -	1,508.74	402.08	06/2016 -	12/2015	-6(O) -	0/19
230	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE	08/2014	288.49 -	288.49	-	02/2017 -	02/2017	0(O) -	0/0
231	SYSTEM STRENGTHENING - XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	232.34	187.19	06/2012 -	-	-	1/3
232	SYSTEM STRENGTHENING - XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,MULTI STATE	09/2012	1,935.35 -	1,935.35	-	12/2014 -	11/2014	-1(O) -	3/13
233	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL,MADHYA PRADESH	03/2012	213.78 -	213.78	153.34	03/2014 -	11/2014	8(O) -	3/7
234	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 -	1,746.65	570.83	08/2014 -	05/2015	9(O) -	1/17
235	SYSTEM STRENGTHENING IN NR FOR SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,022.39	08/2012 -	12/2014	28(O) -	0/6
236	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]PGCIL,MULTI STATE	02/2014	243.53 -	243.53	-	08/2016 -	08/2016	0(O) -	2/20
237	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]PGCIL,MAHARASHTRA	02/2012	1,310.85 -	1,310.85	-	02/2015 -	02/2015	0(O) -	2/14
238	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,MULTI STATE	06/2012	1,263.26 -	1,263.26	-	11/2014 -	11/2014	0(O) -	0/15
239	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATISGARH	01/2012	1,422.85 -	1,422.85	799.32	01/2015 -	06/2015	5(O) -	3/20
240	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 -	297.33	-	08/2014 -	-	-	6/19
241	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	487.49	305.72	06/2014 -	12/2014	6(O) -	7/19
242	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	2,202.00	03/2013 -	03/2018	60(O) -	0/14

Sector Wise Details

(September 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
243	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,WEST BENGAL	09/2005	1,061.38 -	1,929.15	1,551.17	09/2009 -	03/2016	78(O) -	2/5
244	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	909.81	07/2010 02/2016	05/2018	94(O) 27(R)	4/15
245	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118]PGCIL,GUJARAT	01/2012	259.28 -	259.28	169.82	01/2014 -	10/2014	9(O) -	3/16
246	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	1,216.96	08/2014 -	06/2015	10(O) -	2/19
247	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	-	10/2014 -	06/2015	8(O) -	3/17
248	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	3,972.68	10/2012 -	12/2015	38(O) -	0/11
249	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,MULTI STATE	02/2009	184.19 -	184.19	161.72	11/2011 -	06/2014	-	0/4
250	TRANS. SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]PGCIL,MULTI STATE	06/2014	400.47 -	400.47	-	05/2017 -	05/2017	0(O) -	0/0
251	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	1,867.60	12/2012 -	06/2015	30(O) -	0/11
252	TRANS. SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]PGCIL,ANDHRA PRADESH	08/2014	188.75 -	188.75	-	02/2017 -	02/2017	0(O) -	0/0
253	TRANS.SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	5,151.37	-	04/2018 -	04/2018	0(O) -	0/0
254	TRANSM SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 -	4,404.57	661.15	01/2015 -	12/2015	11(O) -	6/21
255	TRANSMISSION SYS ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1 - [N18000121]PGCIL,MULTI STATE	02/2012	324.33 -	324.33	-	08/2014 -	-	-	9/19
256	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3&4 - [N18000166]PGCIL,GUJARAT	02/2014	378.71 -	378.71	11.20	10/2016 -	10/2016	0(O) -	0/20
257	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL,MULTI STATE	02/2012	1,927.16 -	1,927.16	-	10/2014 -	10/2014	0(O) -	4/15
258	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL,MULTI STATE	09/2013	1,575.30 -	1,575.30	-	05/2016 -	05/2016	0(O) -	1/18
259	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	437.80	02/2014 -	12/2014	10(O) -	4/16
260	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]PGCIL,MULTI STATE	09/2011	1,366.34 -	1,366.34	1,123.46	12/2013 -	02/2015	14(O) -	7/12
261	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	310.81	11/2013 -	03/2015	16(O) -	6/20

Sector Wise Details

(September 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
262	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 -	2,074.86	1,657.94	03/2013 -	11/2014	20(O) -	5/14
263	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]PGCIL,MULTI STATE	03/2011	2,569.25 -	2,569.25	2,550.67	03/2014 -	02/2015	11(O) -	4/14
264	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19 -	2,743.19	2,368.80	12/2013 -	02/2015	14(O) -	2/12
265	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	-	01/2013 -	06/2015	29(O) -	5/21
266	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,319.96	11/2013 -	06/2015	19(O) -	4/15
267	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. - [N18000076]PGCIL,MULTI STATE	03/2010	4,672.99 -	4,672.99	3,381.37	11/2012 -	03/2015	28(O) -	0/10
268	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH	11/2011	2,127.51 -	2,127.51	1,943.33	07/2014 -	03/2015	8(O) -	2/13
269	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 623.44	994.85	833.58	07/2013 08/2014	11/2014	16(O) 3(R)	21/25
270	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM	01/2011	368.72 -	913.63	656.12	07/2006 12/2015	02/2015	103(O) -10(R)	2/13
271	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	-	04/2016 -	04/2016	0(O) -	0/0
272	VINDHYACHAL STPP STAGE-V - [N18000134]NTPC,MADHYA PRADESH	12/2011	3,180.40 -	3,180.40	1,234.00	08/2015 -	08/2015	0(O) -	19/19
273	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,UTTARAKHAND	08/2008	2,491.58 3,745.08	3,745.08	498.11	07/2014 -	07/2018	48(O) -	1/1
274	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 -	477.69	495.59	09/2010 -	12/2014	51(O) -	0/7
275	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATISGARH	03/2012	9,569.76 -	9,569.76	-	06/2015 -	12/2015	6(O) -	4/28
	Total		244,305.12 -	259,040.96	118,701.27				424/1441
	RAILWAYS								
276	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP,TELANGANA	04/2012	632.68 -	816.55	17.42	04/2012 03/2016	03/2018	71(O) 24(R)	0/0
277	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]JR,MAHARASHTRA	04/2011	182.06 -	184.06	5.15	- -	-	-	0/0
278	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,TRIPURA	04/2008	813.34 -	1,741.00	752.27	03/2014 -	03/2018	48(O) -	0/0
279	AGARTALA-AKHAURA NL - [N22000195]NEFR,TRIPURA	04/2012	252.00 -	252.00	-	- -	-	-	0/0
280	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	432.72	414.84	12/2009 03/2011	12/2014	60(O) 45(R)	0/0
281	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	567.18	2.67	- -	-	-	0/0

Sector Wise Details

(September 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
282	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	385.60	61.92	03/2013 -	-	-	0/0
283	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	2,820.00	329.26	- -	-	-	0/0
284	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	218.39	24.14	- -	-	-	0/0
285	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	822.00	-	- -	-	-	0/0
286	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCOR,MULTI STATE	04/2008	184.26 -	2,000.00	17.32	- -	-	-	0/0
287	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,MULTI STATE	12/2006	170.00 -	485.00	417.70	03/2011 -	-	-	0/0
288	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	242.09	-	- -	-	-	0/0
289	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	338.54	122.62	- -	-	-	0/0
290	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NEFR,ASSAM	04/2011	312.12 -	312.12	107.90	- -	03/2017	-	0/0
291	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 663.01	725.00	575.94	06/1999 -	-	-	0/0
292	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	295.68	0.81	- -	-	-	0/0
293	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	307.00	-	- -	-	-	0/0
294	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	1,566.00	138.10	- -	-	-	0/0
295	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	490.80	0.39	- -	-	-	0/0
296	ARARIA-SUPAUL (NL) - [N22000177]EJR,BIHAR	04/2008	304.41 -	304.41	0.19	- -	-	-	0/0
297	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	528.00	2.96	- -	-	-	0/0
298	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	199.75	57.85	- -	-	-	0/0
299	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	986.30	55.24	- -	-	-	0/0
300	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	288.35	9.54	- -	-	-	0/0
301	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 -	207.52	215.45	12/2012 -	-	-	0/0
302	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	02/1999	138.00 -	1,382.78	0.79	- -	-	-	0/0
303	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	246.08	2.95	- -	-	-	0/0
304	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,WEST BENGAL	03/1998	111.90 1,039.29	1,423.98	483.57	03/2005 12/2008	-	-	0/0
305	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	1,106.62 -	1,106.62	242.64	12/2010 -	-	-	0/0

Sector Wise Details

(September 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
306	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	450.55	13.19	- -	-	-	0/0
307	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64 -	255.64	-	- -	-	-	0/0
308	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP, MAHARASHTRA	03/1996	401.81 495.44	1,814.10	392.88	03/2004 12/2010	03/2016	144(O) 63(R)	0/0
309	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCOR,MULTI STATE	04/2010	337.49 -	337.50	7.75	- -	-	-	0/0
310	BHADRACHALAM-KOVVUR - [N22000264]SCOR,MULTI STATE	04/2012	923.23 -	923.23	0.36	- -	-	-	0/0
311	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR, ODISHA	03/2013	858.67 -	858.67	0.66	- -	-	-	0/0
312	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL	04/2011	289.64 -	289.64	0.09	- -	-	-	0/0
313	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR, MIZORAM	04/2008	619.34 -	2,393.48	192.81	04/2014 03/2020	03/2020	71(O) 0(R)	0/0
314	BHANUPALI-BILASPUR BERI NL - [N22000273]NR, HIMACHAL PRADESH	04/2008	1,046.88 -	2,966.99	40.80	- -	-	-	0/0
315	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR, GUJARAT	04/2006	117.36 196.95	196.95	198.66	03/2011 -	-	-	0/0
316	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER, UTTAR PRADESH	03/2008	195.64 -	195.64	82.20	- -	-	-	0/0
317	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, MADHYA PRADESH	09/2007	687.20 -	800.00	798.47	03/2010 -	12/2015	69(O) -	0/0
318	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR, GUJARAT	04/2008	318.24 -	321.62	2.27	03/2012 -	-	-	0/0
319	BIHTA-AURANGABAD (NL) - [N22000170]ECOR, BIHAR	04/2008	326.20 -	326.20	1.68	- -	-	-	0/0
320	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER, MULTI STATE	04/2011	175.80 -	175.80	1.46	- -	-	-	0/0
321	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	267.37	34.31	- -	-	-	0/0
322	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES, NEFR - [220100201]NEFR, ASSAM	09/1997	1,500.00 -	4,996.19	3,326.02	04/2008 03/2014	06/2017	110(O) 39(R)	0/0
323	CALICUT-MANGALORE (DL) (SR) - [220100151]SR, MULTI STATE	02/1996	240.00 -	579.37	599.40	- -	02/2012	-	0/0
324	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER, ODISHA	04/2010	149.90 -	184.91	64.70	03/2015 -	12/2016	21(O) -	0/0
325	CHANDIGARH-BADDI NL - [N22000296]NR, MULTI STATE	04/2007	328.14 -	328.14	0.17	- -	-	-	0/0
326	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER, MULTI STATE	04/2003	337.96 -	337.96	61.01	- -	-	-	0/0
327	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR, TAMIL NADU	04/2007	247.00 -	951.24	590.71	- -	03/2015	- -	0/0
328	CHENGANNUR-CHINGAVANAM - [N22000203]SR, KERALA	04/2006	191.72 -	222.95	122.80	- -	-	-	0/0

Sector Wise Details

(September 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
329	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1999	271.24 -	520.00	462.38	- -	-	-	0/0
330	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	1,200.00	2.04	- -	-	-	0/0
331	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	494.92	3.66	- -	-	-	0/0
332	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	378.56	106.98	- -	-	-	0/0
333	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,BIHAR	03/2005	470.09 1,417.97	1,417.97	1,011.09	- -	03/2012	-	0/0
334	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	585.93	194.91	- -	12/2013	-	0/0
335	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	243.78	27.74	- -	-	-	0/0
336	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	367.77	-	- -	-	-	0/0
337	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	692.43	-	- -	-	-	0/0
338	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	595.91	89.60	- -	-	-	0/0
339	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	1,347.26	157.55	- -	-	-	0/0
340	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	573.78	166.84	- -	-	-	0/0
341	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NEFR,TRIPURA	04/1999	895.00 -	1,242.25	994.65	03/2007 -	03/2016	108(O) -	0/0
342	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	556.64	268.22	- -	-	-	0/0
343	CUMBUM-PRODDATUR - [N22000282]SCOR,ANDHRA PRADESH	04/2013	829.00 -	829.00	-	- -	-	-	0/0
344	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	1,640.04	168.79	- -	-	-	0/0
345	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	259.51 -	533.38	113.76	12/2011 -	-	-	0/0
346	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL, CHHATISGARH	04/1995	304.00 -	968.60	-	12/2012 -	-	-	0/0
347	DANGOAPSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 -	388.67	111.16	12/2015 -	03/2016	3(O) -	0/0
348	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	406.92	153.62	- -	-	-	0/0
349	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	296.44	4.55	- -	-	-	0/0
350	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	205.00	5.20	- -	-	-	0/0
351	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	410.08	253.22	- -	-	-	0/0

Sector Wise Details

(September 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
352	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	165.16	106.62	03/2015 -	03/2015	0(O) -	0/0
353	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	1,239.00	-	- -	-	-	0/0
354	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	336.91	143.30	- -	-	-	0/0
355	DEOGHAR - SULTANGANJ (NL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	607.09	562.56	12/2012 12/2012	-	-	0/0
356	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	376.59	2.67	- -	-	-	0/0
357	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 2,030.50	2,030.50	2.43	02/2019 -	02/2019	0(O) -	0/0
358	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 -	651.17	7.23	- -	-	-	0/0
359	DIMAPUR-TIZIT NL - [N22000196]NEFR,NAGALAND	04/2013	4,274.00 -	4,274.00	-	- -	-	-	0/0
360	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	914.98	806.89	- -	03/2015	-	0/0
361	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	4,874.58	1,741.00	03/2016 -	03/2016	0(O) -	0/0
362	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	272.39	141.55	03/2012 12/2013	03/2015	36(O) 15(R)	0/0
363	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	189.24	1.52	- -	-	-	0/0
364	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	603.22	1.49	- -	-	-	0/0
365	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	09/2001	120.00 245.39	245.39	232.11	12/2008 -	12/2014	72(O) -	0/0
366	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	495.74	286.16	06/2013 06/2013	-	-	0/0
367	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	654.00	-	- -	-	-	0/0
368	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,MULTI STATE	03/1984	520.00 835.04	835.04	646.73	03/1995 -	03/2015	240(O) -	0/0
369	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	1,922.00	0.55	- -	-	-	0/0
370	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	270.00	303.20	02/2011 02/2011	-	-	0/0
371	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	415.67	13.98	- -	-	-	0/0
372	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	445.25	1.14	- -	-	-	0/0
373	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	197.73	-	- -	-	-	0/0
374	GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL	04/2009	611.03 -	611.03	140.10	12/2011 11/2013	11/2013	-	0/0
375	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	261.70 -	261.70	156.22	02/2006 -	12/2015	118(O) -	0/0

Sector Wise Details

(September 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
376	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,UTTAR PRADESH	03/2002	863.23 -	1,072.51	874.58	- -	03/2015	- -	0/0
377	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,038.00	1,038.00	590.26	03/1998 -	-	-	0/0
378	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	156.65	53.29	- -	-	-	0/0
379	GUDUR-DURGARA JAPATNAM - [N22000265]SCOR,ANDHRA PRADESH	04/2011	283.54 -	283.54	0.31	- -	-	-	0/0
380	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	844.00	621.23	- 05/2009	03/2015	- 70(R)	0/0
381	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	608.02	593.82	03/1994 -	10/2014	247(O) -	0/0
382	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	206.22	17.01	- -	-	-	0/0
383	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 3,845.60	3,845.60	1.92	02/2020 -	02/2020	0(O) -	0/0
384	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	157.17	76.90	- -	-	-	0/0
385	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	213.01	9.70	- -	-	-	0/0
386	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	324.66	202.86	- -	-	-	0/0
387	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	267.09	1.50	- -	-	-	0/0
388	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	172.03	5.86	- -	-	-	0/0
389	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	1,185.64	-	- 09/2009	-	-	0/0
390	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	329.97	1.74	- -	-	-	0/0
391	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N22000052]WS&PU,BIHAR	04/2003	98.74 224.51	337.30	222.07	- -	03/2012	-	0/0
392	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 -	1,289.92	926.17	- -	-	-	0/0
393	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	230.03	161.08	- -	-	-	0/0
394	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	829.74	75.09	03/2015 -	03/2015	0(O) -	0/0
395	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	400.00	-	- -	-	-	0/0
396	HOSADURGA - CHICKJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA	04/2010	203.40 -	203.40	88.25	- -	-	-	0/0
397	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	2,127.00	47.50	- -	-	-	0/0
398	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	157.94	42.46	- -	-	-	0/0
399	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	445.40	180.72	03/2007 03/2007	03/2015	96(O) 96(R)	0/0

Sector Wise Details

(September 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
400	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	166.89	0.02	- -	-	-	0/0
401	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	2,135.00	108.42	- -	-	-	0/0
402	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	313.24	194.17	01/1999 -	-	-	0/0
403	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	653.46	245.91	03/2014 -	-	-	0/0
404	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	162.96	142.23	- -	-	-	0/0
405	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	847.75	831.24	06/2007 -	-	-	0/0
406	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 335.77	1,043.56	749.25	03/2012 -	-	-	0/0
407	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	470.00	14.00	- -	-	-	0/0
408	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	201.17	218.68	- -	-	-	0/0
409	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	740.00	588.78	03/2012 03/2012	12/2012	-	0/0
410	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,MANIPUR	04/2003	727.56 727.56	5,996.00	2,519.80	03/2011 03/2014	03/2018	84(O) 48(R)	0/0
411	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	2,050.00	188.72	- -	11/2014	-	0/0
412	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	923.52	208.10	- -	-	-	0/0
413	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	174.56	55.93	- -	-	-	0/0
414	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	279.70	4.40	- -	-	-	0/0
415	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,062.36	1,651.54	1,604.79	- -	03/2015	-	0/0
416	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	643.00	-	- -	-	-	0/0
417	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	744.71 -	744.71	570.12	- -	-	-	1/1
418	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	800.00	777.39	- -	-	-	0/0
419	KATAKHAL TO BHAIRABI - [N22000126]NEFR,ASSAM	04/1998	227.90 -	331.40	174.44	12/2012 -	03/2016	39(O) -	0/0
420	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,BIHAR	09/2001	492.98 -	1,022.64	744.08	12/2010 -	-	-	0/0
421	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66 -	423.66	215.50	03/2017 -	03/2017	0(O) -	0/0

Sector Wise Details

(September 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
422	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCOR,MULTI STATE	04/2012	1,054.35 -	1,054.35	1.36	- -	-	-	0/0
423	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	162.87	134.34	- -	-	-	0/0
424	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	276.00	-	03/2009 03/2009	08/2014	-	0/0
425	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	1,995.25	328.73	- -	-	-	0/0
426	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 -	826.57	174.31	- -	-	-	0/0
427	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,BIHAR	04/2008	282.92 -	359.86	2.22	- -	-	-	0/0
428	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87 -	768.87	559.58	- 03/2010	03/2010	-	0/0
429	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	2,957.21 -	2,957.21	1,844.66	07/2005 -	-	-	0/0
430	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	418.17	236.07	- -	-	-	0/0
431	KONDAPALLI-PENUBALLI - [N22000260]SCOR,MULTI STATE	04/2013	723.00 -	723.00	-	- -	-	-	0/0
432	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	341.41	296.78	03/2012 -	-	-	0/0
433	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	1,045.20	0.03	- -	-	-	0/0
434	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	252.96	1.52	- -	-	-	0/0
435	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	192.56	0.38	- -	-	-	0/0
436	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	346.15	14.82	- -	-	-	0/0
437	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1999	406.99 -	406.99	141.55	- -	-	-	0/0
438	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	1,630.97	454.39	05/2008 -	-	-	0/0
439	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	257.42	69.55	03/2014 -	03/2014	-	0/0
440	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NEFR,ASSAM	04/2012	246.07 -	364.06	0.30	- -	-	-	0/0
441	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NEFR,ASSAM	04/1996	1,676.31 -	5,185.44	4,452.04	03/2009 -	03/2016	84(O) -	0/0
442	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	480.00	2.76	07/2008 -	07/2008	-	0/0
443	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	450.00	15.05	- -	-	-	0/0
444	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	800.00	0.54	- -	-	-	0/0

Sector Wise Details

(September 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
445	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	493.96	121.27	- -	-	-	0/0
446	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	347.50	207.04	- -	-	-	0/0
447	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	900.05	847.91	12/2011 12/2010	-	-	0/0
448	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	378.56 -	791.59	6.40	- -	-	-	0/0
449	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 -	315.13	1.61	- -	12/2017	-	0/0
450	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	369.00	105.34	- -	-	-	0/0
451	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 332.92	477.88	468.91	03/2012 -	-	-	0/0
452	MANUGURU-RAMAGUNDAM - [N22000259]SCOR,TELANGANA	04/2013	1,112.00 -	1,112.00	-	- -	-	-	0/0
453	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	285.57	1.95	01/1999 -	-	-	0/0
454	MAVLI JN.-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	855.16	557.65	- -	-	-	0/0
455	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	1,383.45	442.35	- -	-	-	0/0
456	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	377.44	3.53	- -	-	-	0/0
457	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	439.88	0.78	- -	-	-	0/0
458	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	468.48	0.83	01/1999 -	-	-	0/0
459	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	276.69	-	01/1999 -	-	-	0/0
460	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	250.93	0.14	- -	-	-	0/0
461	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	211.00	4.51	- -	-	-	0/0
462	MUDKHED-PARBHANI - [N22000283]SCOR,MAHARASHTRA	04/2011	390.60 -	390.60	3.84	- -	-	-	0/0
463	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 6,213.84	7,012.84	1,820.40	03/2014 03/2019	03/2019	60(O) 0(R)	0/0
464	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 236.41	645.00	305.66	- -	12/2014	-	0/0
465	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	1,350.91	295.46	- -	-	-	0/0
466	MURKONGSELEK-PASIGHAT NL - [N22000208]NEFR,MULTI STATE	04/2011	165.82 -	545.64	0.54	- -	-	-	0/0
467	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	281.30	0.58	- -	-	-	0/0

Sector Wise Details

(September 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
468	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	228.05	0.02	- -	-	-	0/0
469	NADIKUDE-SRI KALAHASTI - [N22000286]SCOR,ANDHRA PRADESH	04/2011	1,313.48 -	1,313.48	4.48	- -	-	-	0/0
470	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	883.00	721.20	02/2009 -	03/2012	-	0/0
471	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	37.68 -	1,036.78	404.01	07/2012 -	-	-	0/0
472	NAWADA-LAXMIPUR (NL) - [N22000167]SER,BIHAR	04/2008	620.57 -	620.57	-	- -	-	-	0/0
473	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	494.54	31.20	- -	-	-	0/0
474	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NEFR,BIHAR	09/2006	300.00 -	532.87	51.80	- -	-	-	0/0
475	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NEFR,ASSAM	09/2006	200.00 -	430.33	204.17	- -	03/2017	-	0/0
476	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NEFR,MULTI STATE	04/2010	242.22 -	242.22	39.70	- -	-	-	0/0
477	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NEFR,MEGHALAYA	04/2010	4,083.02 -	4,083.02	7.30	- -	-	-	0/0
478	NEW BG LINE FROM DUDHNOI-MENDIPATAR - [N22000192]NEFR,MULTI STATE	04/1999	175.43 -	247.75	240.20	- -	-	-	0/0
479	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NEFR,MULTI STATE	04/2010	241.52 -	241.52	233.46	- -	-	-	0/0
480	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NEFR,WEST BENGAL	04/2010	221.42 -	221.42	21.43	- -	-	-	0/0
481	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NEFR,WEST BENGAL	04/1983	36.80 274.41	703.18	255.54	- -	-	-	0/0
482	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NEFR,MULTI STATE	04/2013	1,798.00 -	1,798.00	-	- -	-	-	0/0
483	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NEFR,WEST BENGAL	04/2011	209.77 -	209.77	75.14	- -	03/2017	-	0/0
484	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NEFR,WEST BENGAL	04/2012	283.55 -	283.55	8.02	- -	03/2017	-	0/0
485	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NEFR,MULTI STATE	04/1999	523.17 -	1,418.21	1,038.30	- -	-	-	0/0
486	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NEFR,NAGALAND	04/2006	850.00 -	2,446.57	10.23	03/2015 03/2020	03/2020	60(O) 0(R)	0/0
487	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NEFR,MULTI STATE	04/2000	733.00 733.00	2,483.04	1,673.08	12/2008 -	03/2016	87(O) -	0/0
488	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	2,298.42	78.05	03/2014 -	03/2016	24(O) -	0/0

Sector Wise Details

(September 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
489	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	2,913.51	382.68	03/2016 -	03/2016	0(O) -	0/0
490	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	121.21	03/2016 -	06/2016	3(O) -	0/0
491	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 4,259.48	4,259.48	733.02	03/2016 -	03/2016	0(O) -	0/0
492	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, ANDHRA PRADESH	07/2006	743.00 -	1,117.11	-	03/2008 06/2008	-	-	0/0
493	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR, GUJARAT	04/2013	1,266.89 -	1,266.89	-	-	-	-	0/0
494	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	293.74 -	293.74	139.96	12/2010 -	-	-	0/0
495	PANVEL PEN DOUBLING - [N22000255]CR, MULTI STATE	04/2006	96.16 -	260.16	232.37	-	-	-	0/0
496	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR, BIHAR	04/2001	624.47 -	2,921.00	2,252.44	10/2007 12/2012	12/2015	98(O) 36(R)	0/0
497	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, TELANGANA	12/1994	124.43 -	925.30	697.54	-	02/2014	-	0/0
498	PEN ROHA DOUBLING - [N22000254]CR, MULTI STATE	04/2007	98.74 -	203.00	214.24	-	03/2015	-	0/0
499	PIRPAINTI-BHAGALPUR - [N22000222]ER, MULTI STATE	04/2011	261.38 -	261.38	21.21	-	-	-	0/0
500	PIRPAINTI-JASIDIH - [N22000219]ER, MULTI STATE	04/2013	915.98 -	915.98	0.09	-	-	-	0/0
501	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER, MULTI STATE	04/2011	248.07 -	248.07	26.60	03/2015 -	03/2015	0(O) -	0/0
502	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER, MULTI STATE	04/2011	299.60 -	299.60	1.10	03/2017 -	03/2017	0(O) -	0/0
503	PUSHKAR-MERTA - [N22000151]NWR, RAJASTHAN	04/2013	323.00 -	323.00	-	-	-	-	0/0
504	QADIAN-BEAS - [N22000295]NR, PUNJAB	04/2011	205.22 -	205.22	1.54	-	-	-	0/0
505	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR, TAMIL NADU	04/1999	460.94 -	1,030.00	804.20	01/1999 -	-	-	0/0
506	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR, MULTI STATE	03/1998	280.00 -	1,122.00	871.73	-	-	-	0/6
507	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL, ANDHRA PRADESH	04/2003	136.62 -	289.93	-	12/2007 03/2010	-	-	0/0
508	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR, BIHAR	04/2002	921.00 -	2,363.00	1,473.59	03/2009 12/2012	12/2014	69(O) 24(R)	0/0
509	RAJATGARH-BARANG(LD), ECR - [220100286]RVNL, ODISHA	04/1999	166.16 -	288.00	-	02/2009 02/2009	08/2014	-	0/0
510	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER, JHARKHAND	04/2012	148.77 -	174.69	1.80	12/2016 -	12/2016	0(O) -	0/0
511	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR, GUJARAT	04/1994	320.66 -	913.48	458.16	-	-	-	0/0

Sector Wise Details

(September 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
512	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	874.57	606.09	03/2013 -	03/2016	36(O) -	0/0
513	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	470.92 727.13	1,225.90	243.71	- -	-	-	0/0
514	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	334.90	230.66	06/2004 -	12/2015	138(O) -	0/0
515	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]NEFR,ASSAM	01/2004	915.70 -	3,019.17	3,045.85	- -	03/2015	-	0/0
516	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	288.97	0.09	- -	-	-	0/0
517	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	872.22	790.03	- -	-	-	0/0
518	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2012	2,082.75 -	2,082.75	31.49	- -	-	-	0/0
519	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	1,421.25	394.53	03/2012 -	-	-	0/0
520	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	1,743.00	299.26	- -	-	-	0/0
521	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	755.54	3.13	- -	-	-	0/0
522	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	714.10	46.02	04/2016 -	04/2016	0(O) -	0/0
523	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	193.44	33.44	- -	-	-	0/0
524	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	325.00	248.56	- -	-	-	0/0
525	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	355.81	349.00	- -	-	-	0/0
526	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	385.54	-	03/2010 -	-	-	0/0
527	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	155.81	15.78	- -	-	-	0/0
528	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 -	1,111.99	26.99	- -	-	-	0/0
529	SANTOSHAPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	268.52	78.81	- -	-	-	0/0
530	SEVOK RANGPO, NEFR - [N22000102]NEFR,SIKKIM	04/2008	1,339.48 -	3,375.42	85.64	12/2015 -	03/2020	51(O) -	0/0
531	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	832.47	0.58	- -	-	-	0/0
532	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	678.62	17.47	- -	-	-	0/0
533	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKAPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	297.47	51.82	- -	-	-	0/0
534	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	277.28	64.85	- -	-	-	0/0

Sector Wise Details

(September 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
535	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	466.65	0.02	- -	-	-	0/0
536	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	1,500.00	0.01	- -	-	-	0/0
537	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA	04/1998	183.23 -	818.29	-	02/2015 -	02/2015	0(O) -	0/0
538	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	450.00	7.77	- -	-	-	0/0
539	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 -	516.23	570.80	03/2014 -	-	-	0/0
540	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	810.78	140.40	- -	-	-	0/0
541	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 -	1,074.45	462.27	06/2005 07/2011	-	-	0/0
542	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	171.02 -	171.02	155.41	06/2013 -	12/2014	18(O) -	0/0
543	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	365.17	1.30	- -	-	-	0/0
544	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	1,188.91	687.57	- 12/2009	-	-	0/0
545	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR,TAMIL NADU	04/2011	190.10 -	190.10	32.87	- -	-	-	0/0
546	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	236.93	-	- -	-	-	0/0
547	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 -	820.00	197.74	- -	-	-	0/0
548	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 -	420.00	66.57	- -	-	-	0/0
549	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	167.73	115.71	03/2012 -	-	-	0/0
550	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 -	900.00	591.30	- -	-	-	0/0
551	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL	03/2000	1,049.69 3,156.32	3,176.10	3,598.21	12/2006 -	-	-	0/0
552	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	167.50	0.18	- -	-	-	0/0
553	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	1,801.01	0.89	- -	-	-	0/0
554	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	19,565.00	9,965.25	11/2002 -	12/2018	193(O) -	0/0
555	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	1,389.62	912.13	03/2014 -	-	-	0/0
556	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	380.00	1.38	- -	-	-	0/0
557	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 -	1,116.53	374.71	03/2010 03/2017	03/2017	84(O) 0(R)	0/0

Sector Wise Details

(September 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
558	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR(221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	-	- -	-	-	0/0
559	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	1,280.83	0.84	- -	-	-	0/0
560	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 -	548.01	199.94	- 03/2010	-	-	0/0
561	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	685.17	140.42	- -	-	-	0/0
562	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	279.40	217.84	- -	-	-	0/0
563	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	2,501.05	75.09	- -	-	-	0/0
564	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	297.85	6.14	- -	-	-	0/0
565	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	348.85	0.34	- -	-	-	0/0
566	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	876.00	-	- -	-	-	0/0
	Total		163,873.51 -	274,821.46	87,781.12				1/7
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
567	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	362.20	08/2013 -	02/2015	18(O) -	0/0
568	2 LANING OF MUZAFFARPUR - SONBARSA - [N24000174]NHAI,BIHAR	05/2011	511.54 -	511.54	65.78	11/2013 -	11/2013	-	0/0
569	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH	10/2012	250.50 -	250.50	363.10	10/2014 -	10/2014	0(O) -	0/0
570	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	373.47	268.60	07/2014 -	11/2014	4(O) -	0/0
571	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	351.54	396.40	05/2013 -	05/2013	-	0/0
572	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	1,179.00	11/2013 -	12/2014	13(O) -	0/0
573	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	624.00	441.40	04/2014 -	05/2015	13(O) -	0/0
574	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]NHAI,MADHYA PRADESH	10/2011	1,565.00 -	1,565.00	1,556.00	10/2014 -	10/2014	0(O) -	0/0
575	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	356.40	250.60	07/2014 -	03/2015	8(O) -	0/0
576	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	141.10	01/2014 -	12/2015	23(O) -	0/0
577	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	226.00	282.30	02/2014 -	02/2014	-	0/0
578	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	664.00	769.50	02/2014 -	02/2014	-	0/0
579	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	406.60	04/2014 -	03/2015	11(O) -	0/0

Sector Wise Details

(September 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
580	2LANING WITH PS GOPALGANJ-CHAPRA - [N24000190]NHAI, BIHAR	12/2011	325.00 -	325.00	171.00	05/2014 -	05/2014	-	0/0
581	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI, GUJARAT	03/2012	828.00 -	828.00	763.50	09/2014 -	03/2015	6(O) -	0/3
582	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI, MULTI STATE	02/2011	2,498.76 -	2,498.76	2,786.00	08/2014 -	07/2015	11(O) -	0/0
583	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI, GUJARAT	12/2010	1,008.50 -	1,008.50	1,381.00	06/2013 -	06/2013	-	0/3
584	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI, KARNATAKA	03/2011	359.00 -	359.00	39.55	09/2013 -	12/2016	39(O) -	0/0
585	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI, GUJARAT	03/2011	785.50 -	785.50	940.50	08/2013 -	08/2013	-	0/3
586	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI, TELANGANA	04/2014	1,266.60 -	1,266.60	-	09/2016 -	09/2016	0(O) -	0/0
587	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI, JHARKHAND	02/2012	398.00 -	398.00	461.90	02/2014 -	09/2015	19(O) -	0/0
588	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, MULTI STATE	02/2011	998.79 -	998.79	1,597.00	08/2013 -	12/2014	16(O) -	0/0
589	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, MULTI STATE	02/2011	1,078.84 -	1,078.84	1,906.00	08/2013 -	06/2015	22(O) -	0/0
590	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI, MULTI STATE	02/2011	580.43 -	580.43	430.20	08/2013 -	12/2015	28(O) -	0/0
591	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI, HARYANA	10/2013	283.25 -	283.25	218.70	10/2015 -	10/2015	0(O) -	0/0
592	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, BIHAR	01/2011	575.00 -	575.00	825.40	07/2013 -	03/2015	20(O) -	0/0
593	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	1,396.18	1,760.00	09/2014 -	09/2014	0(O) -	0/0
594	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI, UTTAR PRADESH	12/2003	348.16 -	465.50	308.10	09/2007 -	06/2015	93(O) -	0/0
595	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI, GUJARAT	01/2013	2,125.24 -	2,125.24	150.20	12/2015 -	12/2015	0(O) -	0/3
596	AMRITSAR-PATHANKOT - [N24000147]NHAI, PUNJAB	05/2010	705.00 -	705.00	2,208.00	11/2012 -	12/2014	25(O) -	0/0
597	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI, TELANGANA	02/2010	390.56 -	390.56	631.70	02/2012 -	06/2013	-	0/0
598	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI, UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	398.50	09/2013 -	12/2015	27(O) -	0/0
599	BARSAT-KRISHNANAGAR - [N24000229]NHAI, WEST BENGAL	08/2012	867.00 -	867.00	598.60	02/2015 -	02/2016	12(O) -	0/0
600	BEAWAR-PALI-PINDWARA - [N24000199]NHAI, RAJASTHAN	12/2011	2,388.00 -	2,388.00	2,249.00	06/2014 -	11/2015	17(O) -	0/0
601	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI, KARNATAKA	12/2010	480.00 -	480.00	664.60	-	10/2014	-	2/2
602	BHOPAL-SANCHI - [N24000192]NHAI, MADHYA PRADESH	10/2011	209.00 -	209.00	38.77	01/2013 -	12/2015	35(O) -	0/0
603	BHUBANESWAR TO PURI - [N24000195]NHAI, ODISHA	03/2011	500.29 -	500.29	632.80	08/2013 -	03/2015	19(O) -	0/0
604	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI, ASSAM	12/2003	237.80 -	237.80	321.40	06/2008 -	03/2015	81(O) -	0/0

Sector Wise Details

(September 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
605	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	195.00	280.20	06/2008 -	03/2015	81(O) -	0/0
606	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	230.00	251.50	06/2005 -	06/2015	120(O) -	0/0
607	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	309.56	258.40	04/2010 01/2016	01/2016	69(O) 0(R)	0/0
608	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	281.31	181.10	02/2010 -	07/2016	77(O) -	0/0
609	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	899.70	03/2013 -	12/2014	21(O) -	0/0
610	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	353.37	446.20	10/2011 -	12/2014	38(O) -	0/0
611	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	572.30	886.90	10/2011 -	06/2015	44(O) -	0/0
612	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	996.80	05/2013 -	12/2014	19(O) -	0/0
613	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	300.00	176.80	10/2008 -	-	-	0/0
614	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	1,928.22	642.90	04/2015 -	04/2015	0(O) -	0/0
615	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	666.40	05/2010 -	12/2014	55(O) -	0/0
616	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	593.00	759.90	07/2013 -	11/2014	16(O) -	0/0
617	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	381.50	06/2013 -	11/2014	17(O) -	0/0
618	DEVIHALLI-HASSAN - [N24000152]NHAI,KARNATAKA	12/2010	453.00 -	453.00	801.40	-	05/2013	-	1/1
619	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	200.00	288.80	06/2008 -	10/2014	76(O) -	0/0
620	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	211.70	05/2008 04/2015	12/2014	79(O) -4(R)	0/0
621	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	232.45	317.20	09/2010 -	03/2015	54(O) -	0/0
622	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	1,573.00	919.30	09/2015 -	09/2015	0(O) -	0/0
623	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	332.94	525.80	09/2008 -	12/2014	75(O) -	0/0
624	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	1,916.79	273.20	11/2016 -	11/2016	0(O) -	0/0
625	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00 -	1,232.00	590.90	08/2015 -	08/2015	0(O) -	0/0
626	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	682.00	729.40	10/2013 -	11/2015	25(O) -	0/0
627	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	201.66	191.70	09/2008 -	12/2014	75(O) -	0/0
628	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	1,141.00	2,157.00	08/2013 -	12/2014	16(O) -	0/0

Sector Wise Details

(September 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
629	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	1,509.10	2,613.00	09/2012 -	12/2014	27(O) -	2/3
630	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	198.16	341.00	04/2008 01/2015	12/2014	80(O) -1(R)	0/0
631	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	175.96	286.70	04/2008 01/2015	12/2014	80(O) -1(R)	0/0
632	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	495.40	12/2009 -	12/2015	72(O) -	0/0
633	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	280.00	366.10	02/2009 -	12/2014	70(O) -	0/0
634	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 331.23	363.74	240.40	07/2009 -	12/2014	65(O) -	0/0
635	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 333.83	386.10	126.70	09/2007 -	03/2015	90(O) -	0/0
636	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	478.00	321.20	10/2013 -	12/2015	26(O) -	0/0
637	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	625.07	995.90	01/2013 -	01/2013	-	0/0
638	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	946.00	737.50	-	-	-	3/3
639	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	325.00	609.50	05/2013 -	12/2015	31(O) -	0/0
640	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	12/2014	20(O) -	0/0
641	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	267.81	698.20	02/2013 -	02/2013	-	0/0
642	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	792.06	1,983.00	12/2012 -	12/2012	-	0/0
643	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	1,173.00	07/2013 -	12/2014	17(O) -	0/0
644	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	746.90	01/2014 -	12/2014	11(O) -	0/0
645	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	927.40	07/2013 -	06/2015	23(O) -	0/0
646	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	795.00	1,132.00	05/2012 -	12/2014	31(O) -	0/0
647	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	250.39	285.30	10/2008 -	11/2014	73(O) -	0/0
648	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	719.20	07/2014 -	12/2015	17(O) -	0/0
649	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,KARNATAKA	09/2010	671.00 -	671.00	1,260.00	-	06/2015	-	2/3
650	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	635.90	608.30	07/2012 -	09/2014	26(O) -	0/0
651	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	280.13	173.80	11/2008 -	06/2015	79(O) -	0/0
652	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	385.13	159.20	04/2009 -	03/2015	71(O) -	0/0
653	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	167.64	138.80	11/2008 -	12/2014	73(O) -	0/0

Sector Wise Details

(September 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
654	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	200.00	207.20	04/2009 -	12/2014	68(O) -	0/0
655	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,415.00	06/2013 -	03/2015	21(O) -	0/0
656	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	591.50	03/2013 -	12/2015	33(O) -	0/0
657	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	264.72	315.70	06/2008 -	12/2014	78(O) -	0/0
658	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19 -	484.19	285.50	10/2014 -	12/2014	2(O) -	0/0
659	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	208.00	334.10	04/2008 04/2015	12/2014	80(O) -4(R)	0/0
660	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	276.40	06/2008 04/2015	03/2015	81(O) -1(R)	0/0
661	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	200.00	281.60	06/2008 -	-	-	0/0
662	NASHRI CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	06/2010	2,159.00 -	2,159.00	622.70	06/2015 -	05/2016	11(O) -	0/0
663	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	1,655.00	655.20	09/2013 -	09/2013	-	0/0
664	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	557.00	1,123.00	02/2010 -	12/2014	58(O) -	0/0
665	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2016	35(O) -	0/0
666	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	787.90	09/2014 -	10/2015	13(O) -	0/0
667	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	03/2015	40(O) -	0/0
668	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00 -	807.00	1,209.43	10/2014 -	10/2014	0(O) -	0/0
669	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	942.69	286.60	06/2014 -	12/2015	18(O) -	0/0
670	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	574.00	982.40	03/2014 -	12/2014	9(O) -	0/0
671	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	632.70	02/2013 -	12/2014	22(O) -	0/0
672	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	940.00	1,601.00	07/2012 -	07/2012	-	0/0
673	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,292.00	03/2013 -	12/2014	21(O) -	0/0
674	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	835.00	475.90	01/2014 -	03/2015	14(O) -	0/0
675	PUNE-SHOLAPUR,PKG1 - [N24000127]NHAI,MAHARASHTRA	11/2009	1,110.00 -	1,110.00	1,826.00	05/2012 -	03/2012	-	0/0
676	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,170.00	07/2015 -	06/2016	11(O) -	0/0
677	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	251.03	384.70	10/2008 -	12/2014	74(O) -	0/0
678	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,MULTI STATE	12/2012	1,479.00 -	1,479.00	354.70	06/2015 -	06/2015	0(O) -	0/0

Sector Wise Details

(September 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
679	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN	03/2012	333.51 -	333.51	270.80	09/2014 -	11/2014	2(O) -	0/0
680	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	650.00	1,178.00	11/2013 -	11/2013	-	0/0
681	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	805.39	841.90	03/2013 -	12/2014	21(O) -	0/0
682	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	909.00	974.30	05/2014 -	12/2014	7(O) -	0/0
683	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 157.47	154.57	267.60	09/2007 03/2014	12/2014	87(O) 9(R)	0/0
684	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, WEST BENGAL	12/2003	225.00 -	225.00	191.00	07/2008 -	-	-	0/0
685	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	1,047.00	294.60	06/2014 -	12/2014	6(O) -	0/0
686	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	535.00	52.18	12/2013 -	03/2015	15(O) -	0/0
687	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,321.00	12/2013 -	12/2014	12(O) -	0/0
688	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	2,188.00	05/2014 -	05/2015	12(O) -	0/0
689	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	156.60	08/2012 -	03/2016	43(O) -	0/0
690	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	245.00	491.20	03/2008 01/2015	10/2014	79(O) -3(R)	0/0
691	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	323.00	06/2014 -	12/2014	6(O) -	0/0
692	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	1,693.75	2,762.00	08/2011 -	12/2014	40(O) -	2/2
693	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	567.00	1,377.00	11/2013 -	11/2013	-	0/0
694	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	-	10/2013 -	11/2014	13(O) -	0/0
695	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	148.80	05/2013 -	12/2014	19(O) -	0/0
696	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,KARNATAKA	11/2010	680.00 -	680.00	383.20	- -	07/2014	-	2/2
697	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,134.00	03/2014 -	12/2015	21(O) -	0/0
698	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI,ANDHRA PRADESH	09/2013	606.00 -	606.00	-	- -	-	-	0/0
699	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	193.45	66.01	11/2012 -	12/2014	25(O) -	0/0
700	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	1,287.95	540.10	11/2015 -	11/2015	0(O) -	0/0
701	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	-	- -	-	-	0/0

Sector Wise Details

(September 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
702	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI,TELANGANA	04/2014	1,123.17 -	1,123.17	-	-	-	-	0/0
	Total		102,321.44 -	104,388.44	95,853.02				14/28
	<u>SHIPPING AND PORTS</u>								
703	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY VESSELS - [N25000014]SHIPP.,MAHARASHTRA	10/2007	359.44 -	359.44	211.30	04/2011 11/2011	11/2011	-	0/0
704	ACQUISITION OF 4 NOS OF 82000 DWT KAMSAVMAX BULK CARRIERS FROM M/S JIANGSU EASTERN HEAVY INDUSTRIES - [N25000051]SHIPP.,MAHARASHTRA	08/2010	612.72 532.83	532.83	505.54	12/2012 11/2013	11/2013	-	0/0
705	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,MULTI STATE	07/2011	220.49 -	220.49	47.32	01/2013 06/2013	06/2013	-	0/0
706	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY - [N25000062]SHIPP.,MULTI STATE	01/2012	511.87 -	511.87	106.72	03/2014 08/2014	08/2014	-	0/0
707	ACQUISITION OF TWO NOS. OF 3060 DWT - [N25000043]SHIPP.,MAHARASHTRA	04/2009	277.03 280.00	277.03	81.40	12/2011 10/2012	10/2012	-	0/0
708	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053]SHIPP.,MAHARASHTRA	10/2010	966.46 -	994.82	427.54	02/2014 01/2015	01/2015	11(O) 0(R)	0/0
709	ACQUISITION OF THREE(3) NOS OF 6500TEU CELLULAR CONTAINER VESSELS FROM M/S STX SHIPBUILDING CO. LTD. - [N25000052]SHIPP.,MAHARASHTRA	10/2010	1,028.10 1,012.23	1,012.23	554.60	12/2013 11/2013	11/2013	-	0/0
710	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 1,460.00	2,098.56	1,020.94	12/2010 09/2012	03/2015	51(O) 30(R)	0/0
711	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,GUJARAT	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	-	0/0
712	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST - [N25000037]PORT TRUST,GUJARAT	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012	-	0/0
713	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL - [N25000003]PORT TRUST,MAHARASHTRA	10/2005	800.00 1,571.60	1,571.60	9.70	10/2008 -	-	-	0/0
714	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,ODISHA	12/2005	154.84 253.36	253.36	221.58	- 01/2009	12/2010	-	0/1
715	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 309.00	600.00	139.80	03/2006 06/2014	06/2014	-	0/0
716	MECHANIZATION OF COAL HANDLING FACILITIES TO 200000 DWT VESSELS ON DBFOT BASIS - [N25000049]PORT TRUST,ANDHRA PRADESH	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	-	0/0
717	MODIFICATION & STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST,GUJARAT	06/2010	277.00 -	277.00	0.21	03/2012 -	03/2012	-	0/0
718	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 298.17	373.22	371.18	04/2009 11/2009	02/2011	-	0/0

Sector Wise Details

(September 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
719	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	2,427.40	831.23	10/2008 11/2010	-	-	0/0
720	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST,GUJARAT	02/2011	830.00 -	621.53	-	05/2013 -	05/2013	-	0/0
	Total		12,117.12 -	14,390.98	4,748.99				0/1
	<u>TELECOMMUNICATIONS</u>								
721	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL,ASSAM	06/2007	336.81 -	336.81	195.94	01/2009 -	12/2014	71(O) -	0/0
722	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	384.00	48.95	10/2010 11/2015	03/2015	53(O) -8(R)	0/0
723	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058]BSNL,UTTARAKHAND	01/2009	149.15 -	158.72	86.05	06/2009 -	12/2014	66(O) -	0/0
724	SUPPLY INSTALLATION TESTING AND COMMISSIONING OF RURAL WIMAX NETWORK PHASE-II - [N26000100]BSNL,MULTI STATE	07/2010	1,148.19 -	964.37	251.27	05/2011 -	06/2014	-	0/0
	Total		2,018.15 -	1,843.90	582.21				0/0
	<u>URBAN DEVELOPMENT</u>								
725	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	-	03/2016 -	05/2016	2(O) -	0/0
726	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD,WEST BENGAL	01/2009	225.81 -	225.81	17.60	06/2012 -	05/2015	35(O) -	0/0
727	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA	05/2006	6,395.00 -	11,609.00	2,267.57	06/2011 -	03/2013	-	3/3
728	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA	02/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019	0(O) -	0/0
729	C/O MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB - [N28000070]CPWD,PUNJAB	08/2005	191.24 -	191.24	8.78	08/2007 -	12/2010	-	0/0
730	C/O MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	165.23	-	10/2012 -	09/2013	-	0/0
731	C/O NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 -	315.00	53.96	06/2015 -	08/2015	2(O) -	0/0
732	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI - [N28000048]CPWD,MAHARASHTRA	11/2006	114.18 173.08	173.08	-	04/2009 -	-	-	0/0
733	CONSTRUCTION OF CENTRAL ACADEMY FOR PUBLIC TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	188.87	10.64	12/2014 -	12/2016	24(O) -	0/0
734	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD,ODISHA	11/2012	238.43 -	238.43	-	02/2015 -	08/2015	6(O) -	0/0
735	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	884.30	103.45	08/2014 -	01/2016	17(O) -	0/0

Sector Wise Details

(September 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
736	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85 -	261.85	101.52	05/2013 -	10/2015	29(O) -	0/0
737	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI	05/2012	405.01 -	405.01	-	12/2014 -	04/2016	16(O) -	0/0
738	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	-	09/2015 -	12/2016	15(O) -	0/0
739	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH	06/2014	157.84 -	157.84	2.04	03/2017 -	03/2017	0(O) -	0/0
740	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	38,585.00	8,699.49	03/2016 -	03/2016	0(O) -	0/0
741	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA - [N28000078]CPWD,BIHAR	11/2006	2,727.89 -	2,727.89	2,637.11	03/2010 -	10/2014	55(O) -	0/0
742	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	15.60	11/2014 -	10/2015	11(O) -	0/0
743	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	1,219.21	-	07/2017 -	07/2017	0(O) -	0/0
744	FARIDABAD EXTENSION - [N28000057]DMRC,DELHI	09/2011	2,494.00 -	2,494.00	685.21	09/2014 -	05/2015	8(O) -	0/0
745	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI - [N28000064]CPWD,DELHI	01/2010	162.90 -	162.90	111.33	07/2012 -	07/2012	-	0/0
746	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 -	241.33	22.43	11/2014 -	11/2014	0(O) -	0/0
747	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]CPWD,BIHAR	02/2012	171.10 -	171.10	85.60	09/2014 -	09/2014	0(O) -	0/0
748	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	332.72	0.08	09/2016 -	09/2016	0(O) -	0/0
749	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	205.00	93.74	03/2012 -	01/2015	34(O) -	0/0
	Total		82,686.31 -	87,959.21	14,916.15				3/3
	<u>WATER RESOURCES</u>								
750	PAGLADIYA DAM PROJECT - [300100001]MOWR,ASSAM	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012	-	0/0
	Total		542.90 -	1,187.00	35.49				0/0
	Grand Total		947,912.88	1,125,673.75	523,833.51				1239/3741


Summary of projects in the Flash Report for the month of September, 2014

Project Implementation - Current Status:

Number of Projects in Previous Month	720
Number of Projects completed/dropped/frozen in Current Month	2
Number of Projects Added in Current Month	32
Number of Projects in Current Month	750


Brief Analysis

Project Status with respect to Original Schedule: Out of 750 projects, 8 projects are ahead of schedule, 110 projects are on schedule and 312 projects are delayed. Of the balance, 302 projects do not have fixed dates of commissioning while 18 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

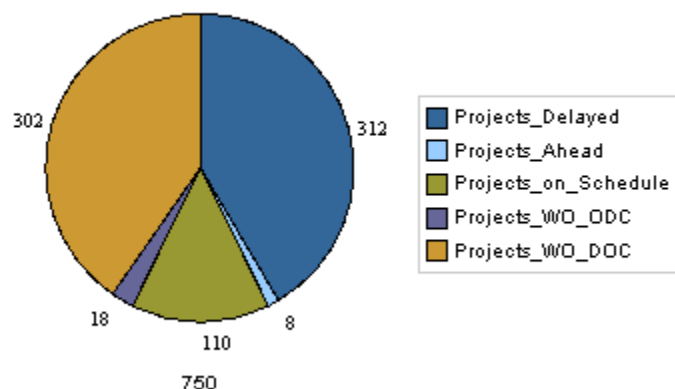

Investment Scenario

Total original cost of implementation of 750 projects when sanctioned, was of the order of Rs. 947912.88 crore but this was subsequently revised to Rs. 1125673.75 crore implying a cost overrun of 18.8%. The expenditure incurred on these projects till September, 2014 is Rs. 523833.51 crore, which is 46.5% of the revised cost of the projects.

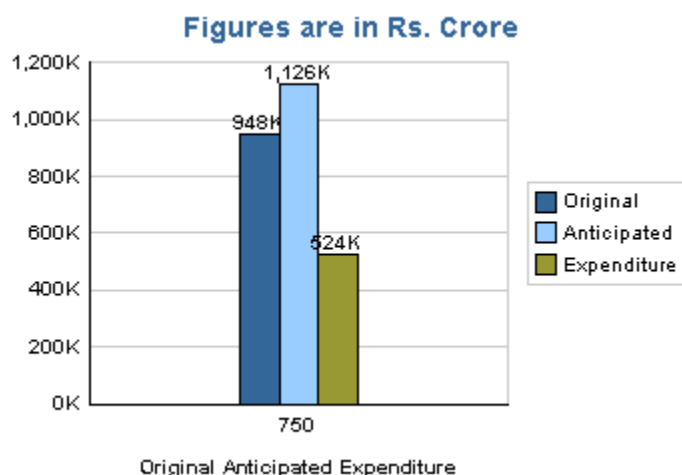

Sector wise current status of projects on the Flash Report

URBAN DEVELOPMENT


Current Status:

Number of Projects	25
Number of Projects On Schedule	7
Number of Projects Delayed	13

Number of Projects Without Date Of Commissioning	5
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 25 projects, 7 projects are on schedule and 13 projects are delayed .5 projects do not have fixed dates of commissioning.

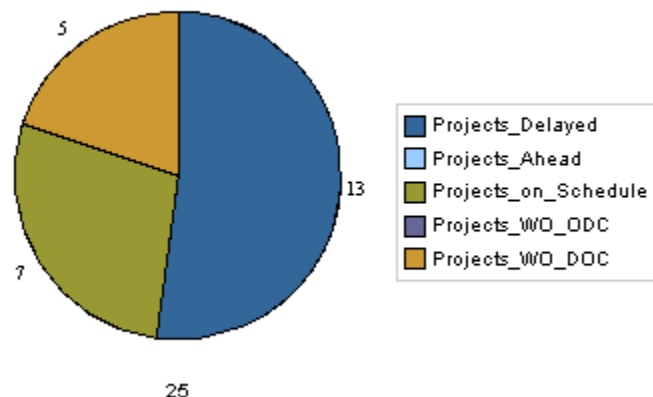

Investment Scenario

Total original cost of implementation of 25 projects when sanctioned, was of the order of Rs. 82686.31 crore but this was subsequently revised to Rs. 87959.21 crore implying a cost overrun of 6.4%. The expenditure incurred on these projects till September, 2014 is Rs. 14916.15 crore, which is 17% of the revised cost of the projects.

Figures are in Rs. Crore

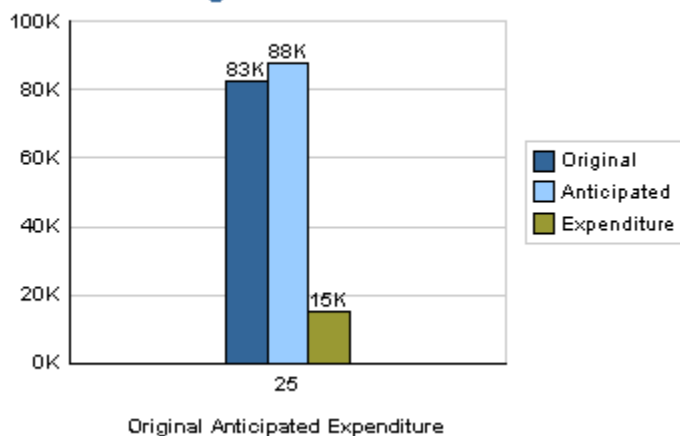

Sector wise current status of projects on the Flash Report


TELECOMMUNICATIONS

Current Status:

Number of Projects	4
Number of Projects Delayed	3
Number of Projects Without Date Of Commissioning	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 3 projects are delayed .1 project do not have fixed dates of commissioning.

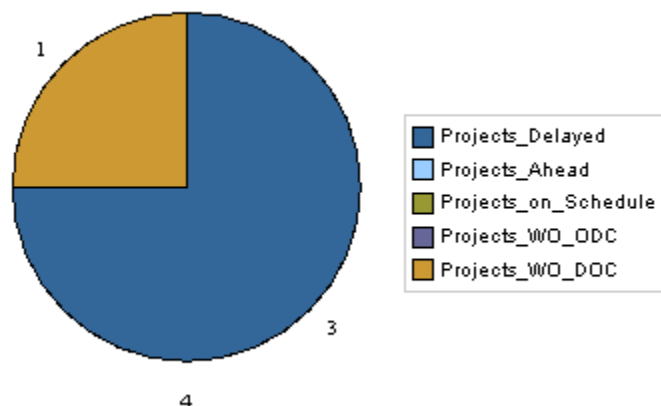

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 2018.15 crore but this was subsequently revised to Rs. 1843.9 crore implying a cost overrun of -8.6%. The expenditure incurred on these projects till September, 2014 is Rs. 582.21 crore, which is 31.6% of the revised cost of the projects.

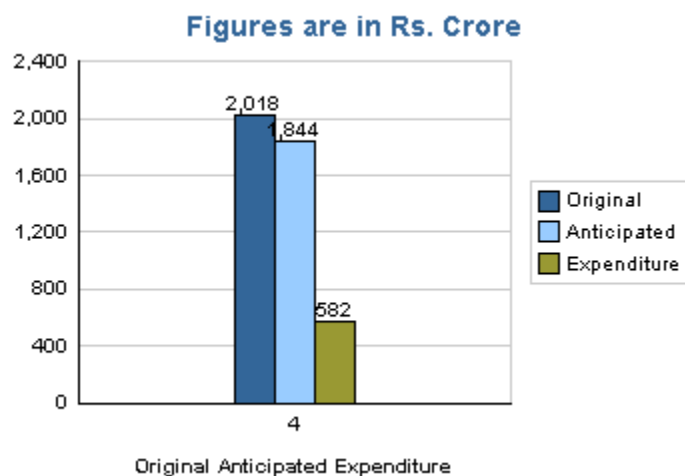

Sector wise current status of projects on the Flash Report

SHIPPING AND PORTS

Current Status:


Number of Projects **18**

Number of Projects Delayed **2**

Number of Projects Without Date Of Commissioning **16**

Brief Analysis


Project Status with respect to Original Schedule: Out of 18 projects, 2 projects are delayed .16 projects do not have fixed dates of commissioning.

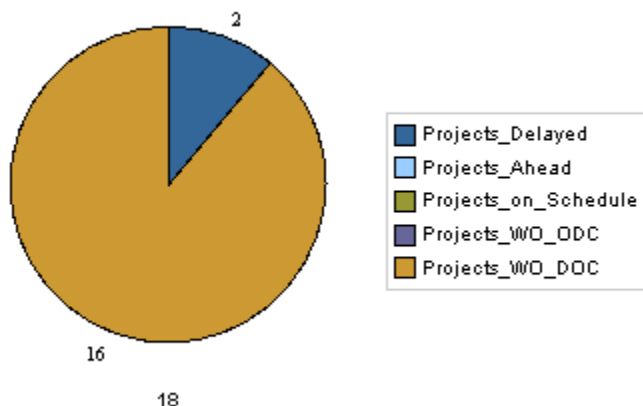

Investment Scenario

Total original cost of implementation of 18 projects when sanctioned, was of the order of Rs. 12117.12 crore but this was subsequently revised to Rs. 14390.98 crore implying a cost overrun of 18.8%. The expenditure incurred on these projects till September, 2014 is Rs. 4748.99 crore, which is 33% of the revised cost of the projects.

Figures are in Rs. Crore

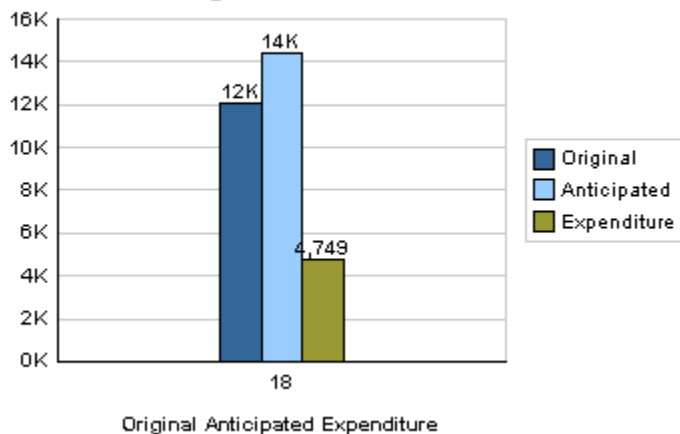

Sector wise current status of projects on the Flash Report

ROAD TRANSPORT AND HIGHW


Current Status:

Number of Projects	136
Number of Projects On Schedule	13
Number of Projects Delayed	96

Number of Projects Without Original Date of Commissioning	2
Number of Projects Without Date Of Commissioning	25

Brief Analysis


Project Status with respect to Original Schedule: Out of 136 projects, 13 projects are on schedule and 96 projects are delayed .25 projects do not have fixed dates of commissioning.2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

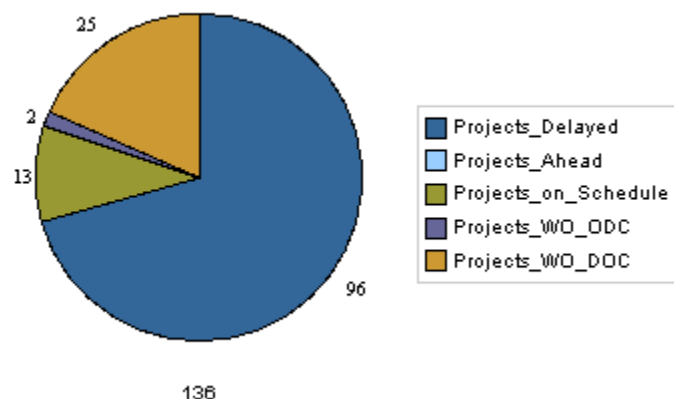

Investment Scenario

Total original cost of implementation of 136 projects when sanctioned, was of the order of Rs. 102321.44 crore but this was subsequently revised to Rs. 104388.44 crore implying a cost overrun of 2%. The expenditure incurred on these projects till September, 2014 is Rs. 95853.02 crore, which is 91.8% of the revised cost of the projects.

Figures are in Rs. Crore

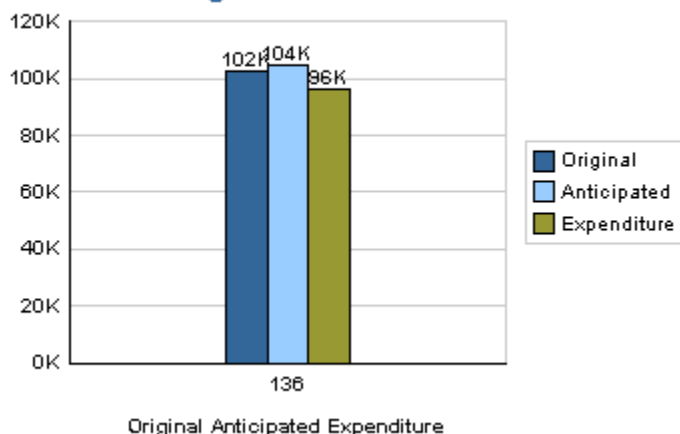

Sector wise current status of projects on the Flash Report

RAILWAYS


Current Status:

Number of Projects	291
Number of Projects On Schedule	13
Number of Projects Delayed	32

Number of Projects Without Original Date of Commissioning	14
Number of Projects Without Date Of Commissioning	232

Brief Analysis


Project Status with respect to Original Schedule: Out of 291 projects, 13 projects are on schedule and 32 projects are delayed .232 projects do not have fixed dates of commissioning.14 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

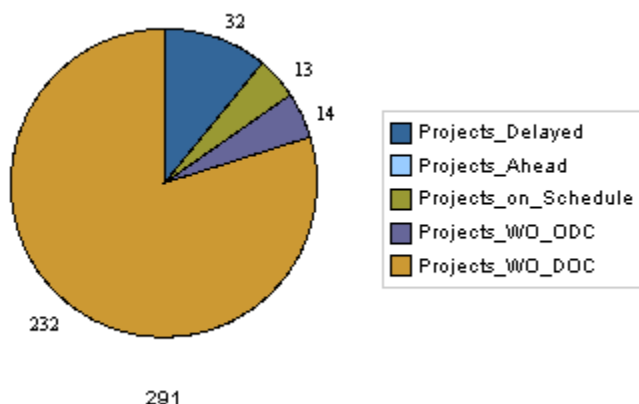

Investment Scenario

Total original cost of implementation of 291 projects when sanctioned, was of the order of Rs. 163873.51 crore but this was subsequently revised to Rs. 274821.46 crore implying a cost overrun of 67.7%. The expenditure incurred on these projects till September, 2014 is Rs. 87781.12 crore, which is 31.9% of the revised cost of the projects.

Figures are in Rs. Crore

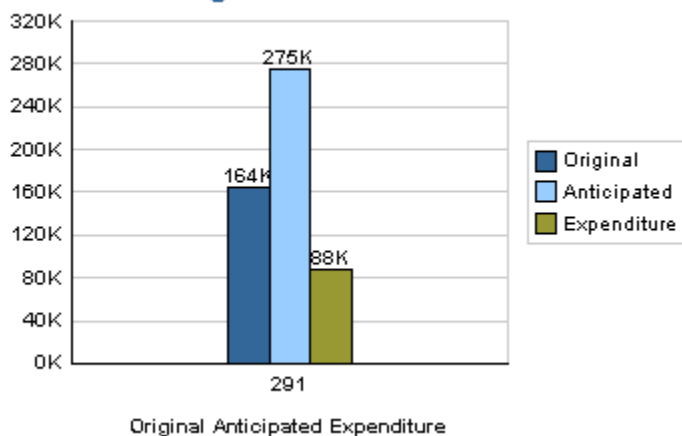

Sector wise current status of projects on the Flash Report


POWER

Current Status:

Number of Projects	102
Number of Projects On Schedule	29
Number of Projects Delayed	56
Number of Projects Ahead	4
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	12

Brief Analysis


Project Status with respect to Original Schedule: Out of 102 projects, 4 projects are ahead of schedule, 29 projects are on schedule and 56 projects are delayed .12 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

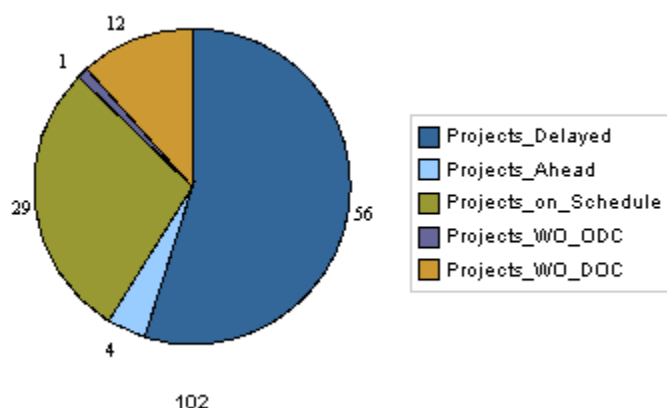

Investment Scenario

Total original cost of implementation of 102 projects when sanctioned, was of the order of Rs. 244305.12 crore but this was subsequently revised to Rs. 259040.96 crore implying a cost overrun of 6%. The expenditure incurred on these projects till September, 2014 is Rs. 118701.27 crore, which is 45.8% of the revised cost of the projects.

Figures are in Rs. Crore

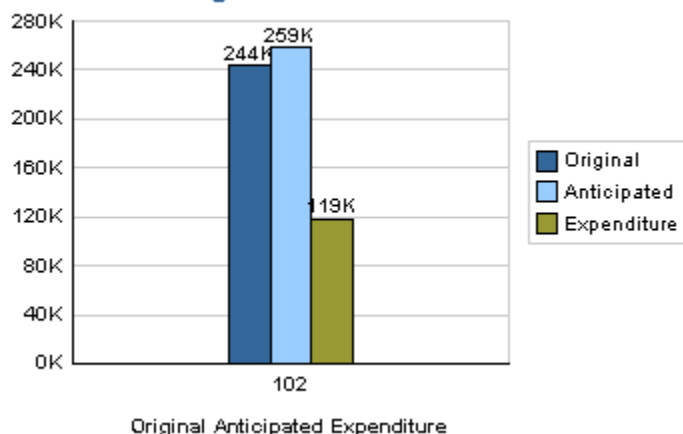

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	78
Number of Projects On Schedule	22
Number of Projects Delayed	48
Number of Projects Ahead	3
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	4


Brief Analysis

Project Status with respect to Original Schedule: Out of 78 projects, 3 projects are ahead of schedule, 22 projects are on schedule and 48 projects are delayed .4 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

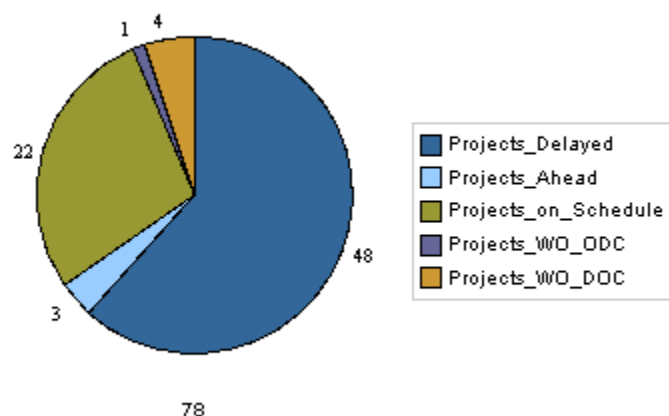

Investment Scenario

Total original cost of implementation of 78 projects when sanctioned, was of the order of Rs. 178906.9 crore but this was subsequently revised to Rs. 195033.69 crore implying a cost overrun of 9%. The expenditure incurred on these projects till September, 2014 is Rs. 78840.32 crore, which is 40.4% of the revised cost of the projects.

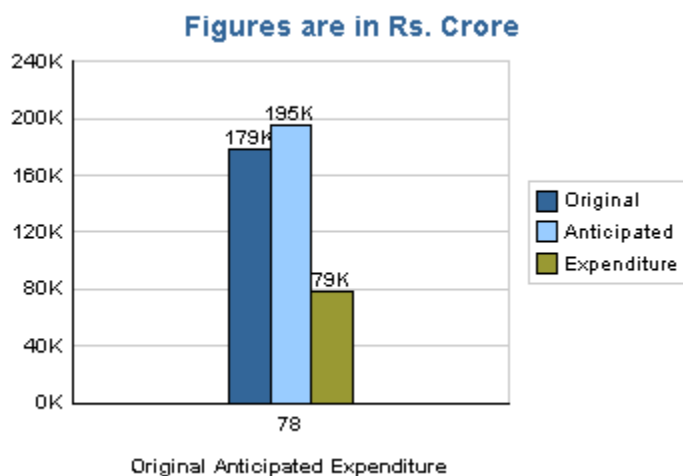

Sector wise current status of projects on the Flash Report


STEEL

Current Status:

Number of Projects	20
Number of Projects On Schedule	4
Number of Projects Delayed	16

Brief Analysis


Project Status with respect to Original Schedule: Out of 20 projects, 4 projects are on schedule and 16 projects are delayed.

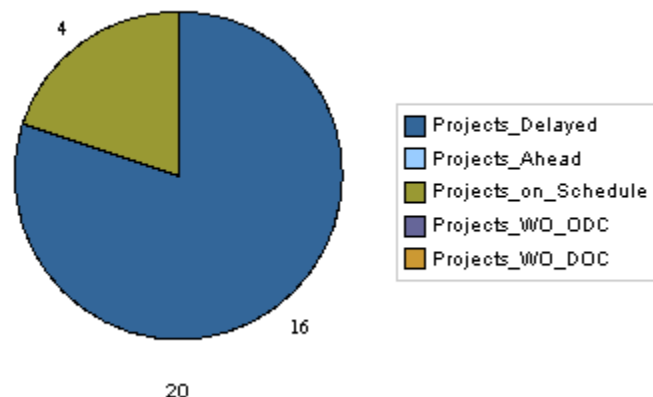

Investment Scenario

Total original cost of implementation of 20 projects when sanctioned, was of the order of Rs. 66395.1 crore but this was subsequently revised to Rs. 72349.06 crore implying a cost overrun of 9%. The expenditure incurred on these projects till September, 2014 is Rs. 61760.12 crore, which is 85.4% of the revised cost of the projects.

Figures are in Rs. Crore

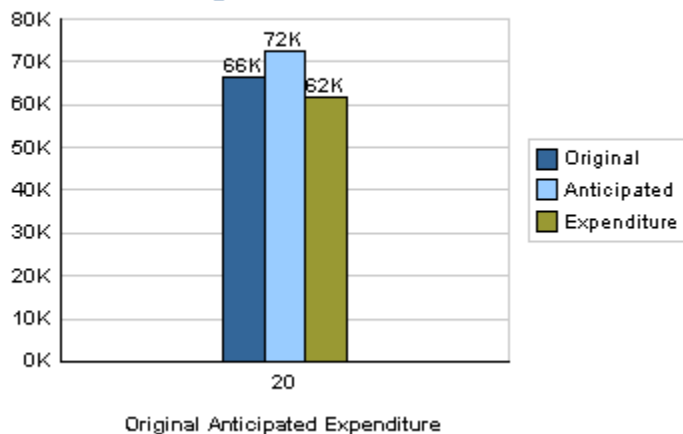

Sector wise current status of projects on the Flash Report

COAL


Current Status:

Number of Projects	64
Number of Projects On Schedule	22
Number of Projects Delayed	38

Number of Projects Without Date Of Commissioning	4
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 64 projects, 22 projects are on schedule and 38 projects are delayed .4 projects do not have fixed dates of commissioning.

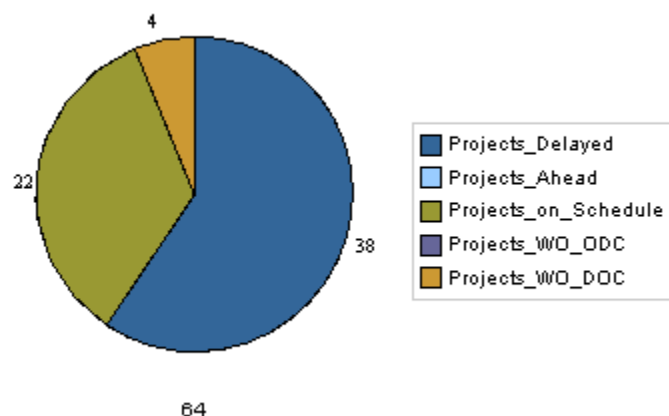

Investment Scenario

Total original cost of implementation of 64 projects when sanctioned, was of the order of Rs. 46558.77 crore but this was subsequently revised to Rs. 56675.18 crore implying a cost overrun of 21.7%. The expenditure incurred on these projects till September, 2014 is Rs. 19996.96 crore, which is 35.3% of the revised cost of the projects.

Figures are in Rs. Crore

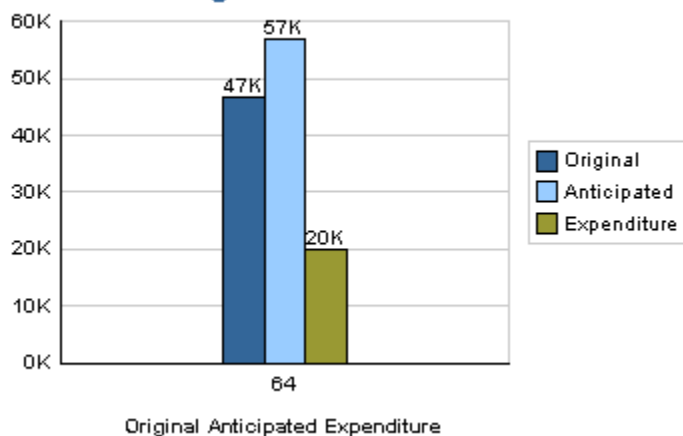

Sector wise current status of projects on the Flash Report


CIVIL AVIATION

Current Status:

Number of Projects	6
Number of Projects Delayed	4
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	1

Brief Analysis


Project Status with respect to Original Schedule: Out of 6 projects, 1 project are ahead of schedule, 4 projects are delayed .1 project do not have fixed dates of commissioning.

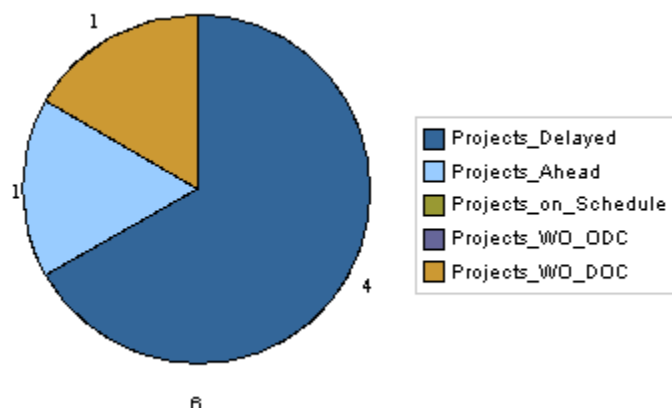

Investment Scenario

Total original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 2284.95 crore but this was subsequently revised to Rs. 2337.87 crore implying a cost overrun of 2.3%. The expenditure incurred on these projects till September, 2014 is Rs. 1383.53 crore, which is 59.2% of the revised cost of the projects.

Figures are in Rs. Crore

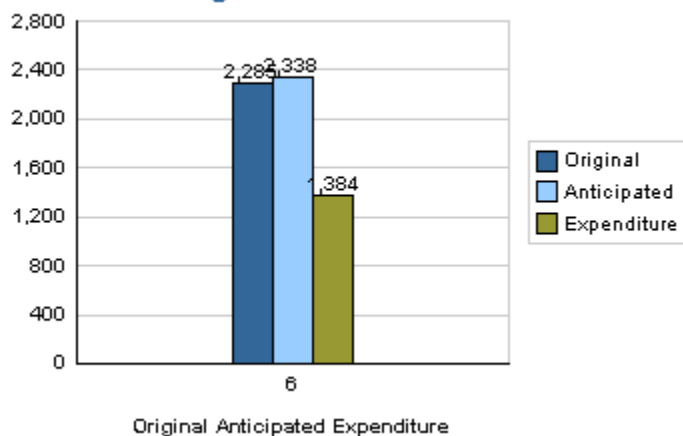

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	4

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed .

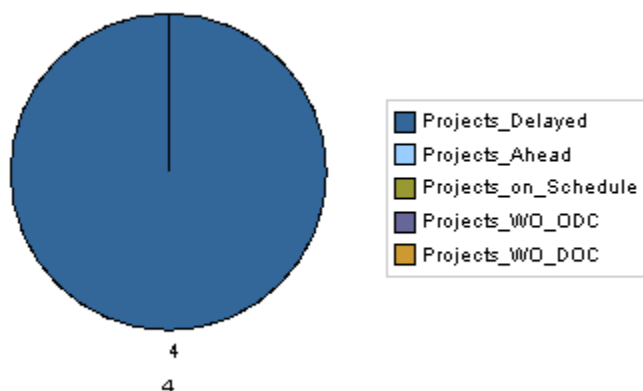

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 40442 crore but this was subsequently revised to Rs. 46726 crore implying a cost overrun of 15.5%. The expenditure incurred on these projects till September, 2014 is Rs. 31310.19 crore, which is 67% of the revised cost of the projects.

Figures are in Rs. Crore

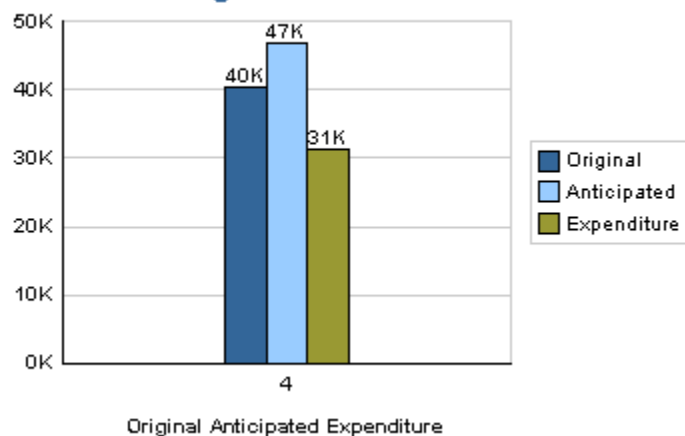

ANNEXURES

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE

(All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	ANDHRA PRADESH	22	24,992.52	30,169.08	20,104.9
2	ARUNACHAL PRADESH	3	9,356.22	12,067.66	11,094.61
3	ASSAM	38	26,930.69	41,738.17	32,483.83
4	BIHAR	48	37,027.18	43,648.73	36,003.6
5	CHANDIGARH	1	452	452	309.21
6	CHHATISGARH	27	58,300.98	65,886.82	25,446.38
7	DELHI	9	44,464.6	44,464.6	9,755.1
8	GOA	1	335.61	388.53	284
9	GUJARAT	33	38,581.24	39,407.29	19,272.11
10	HARYANA	9	4,540.88	6,690.86	7,337.28
11	HIMACHAL PRADESH	6	13,728.27	19,787.64	11,073.97
12	JAMMU AND KASHMIR	7	21,314.62	40,235.3	16,898.29
13	JHARKHAND	31	21,501.51	21,869.27	12,764.5
14	KARNATAKA	34	78,337.98	92,917.96	17,850.74
15	KERALA	12	19,275.88	23,429.66	7,458.68
16	MADHYA PRADESH	17	23,452.88	24,921.57	8,174.07
17	MAHARASHTRA	47	71,517.57	83,936.57	32,355.16
18	MANIPUR	1	727.56	5,996	2,519.8
19	MEGHALAYA	3	4,845.02	4,845.02	1,036.5
20	MIZORAM	2	988.06	3,307.11	848.93
21	MULTI STATE	185	2,00,921.51	2,24,744.27	82,659.14
22	NAGALAND	2	5,124	6,720.57	10.23
23	ODISHA	41	67,166.05	75,819.1	47,850.95
24	PUNJAB	4	1,497.5	1,470.46	2,323.66
25	RAJASTHAN	25	25,638.72	25,695.94	13,970
26	SIKKIM	2	1,648.94	3,684.88	363.55
27	TAMIL NADU	41	53,533.49	70,513.46	46,650.68
28	TELANGANA	21	9,410.31	12,179.13	3,207.66
29	TRIPURA	6	2,966.26	4,780.63	3,076.36
30	UTTAR PRADESH	26	14,207.6	16,863.93	12,005.88
31	UTTARAKHAND	7	9,501.04	13,063.93	4,158.91
32	WEST BENGAL	39	55,626.19	63,977.61	34,484.83
TOTAL		750	9,47,912.88	11,25,673.75	5,23,833.51

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
1	KUDANKULAM APP (NPCIL)	ATOMIC ENERGY	12/2001	13,171	17270	17,894
2	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	COAL	10/2004	2,030.78	3027.59	3,035.56
3	PARBATI HEP (NHPC) II	POWER	09/2002	3,919.59	-	4,667.37
4	SUBANSIRI LOWER H.E.P (NHPC)	POWER	09/2003	6,285.33	-	6,943.84
5	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	POWER	12/2004	2,496.9	-	3,241.37
6	BARH STPP(3X660MW) NTPC	POWER	12/2003	8,692.97	-	10,264
7	TEESTA LOW DAM HEP, STAGE-IV (NHPC)	POWER	09/2005	1,061.38	-	1,551.17
8	VIRANGAM-BHILDI(WR), GC	RAILWAYS	04/1990	155.66	-	199.94
9	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	RAILWAYS	12/1994	124.43	-	697.54
10	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	RAILWAYS	03/1995	2,500	3000	9,965.25
11	CALICUT-MANGALORE (DL) (SR)	RAILWAYS	02/1996	240	-	599.4
12	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR	RAILWAYS	02/1997	295	-	926.17
13	NANGALDAM-TALWARA(NL), NR	RAILWAYS	03/1981	37.68	-	404.01
14	KARUR-SALEM(NL), SR	RAILWAYS	02/1997	155.55	-	777.39

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
15	NANDYAL - YERRAGUNTLA(NL), SCR	RAILWAYS	03/1996	155.74	164.36	721.2
16	KANPUR-KASGANJ-MATHURA(GC), NER	RAILWAYS	03/1997	677.97	1062.36	1,604.79
17	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES, NEFR	RAILWAYS	09/1997	1,500	-	3,326.02
18	MUNEERABAD-MAHABOBNAGAR(NL), SCR	RAILWAYS	04/1997	218.24	236.41	305.66
19	RANCHI-LOHARDAGA(GC), SER	RAILWAYS	04/1997	194.07	-	230.66
20	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	RAILWAYS	09/1998	247.66	-	454.39
21	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	RAILWAYS	04/1997	501.69	335.77	749.25
22	KATI HAR - JOGBANI (GC)(NEFR)	RAILWAYS	09/2001	492.98	-	744.08
23	GULBARGA-BIDAR, SCR(NL)	RAILWAYS	02/1998	242.42	369.7	621.23
24	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER)	RAILWAYS	03/2002	863.23	-	874.58
25	JALANDHAR-PATHANKOT-JAMMU-TAWI(LD), NR	RAILWAYS	03/2002	625.3	408.76	831.24
26	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	RAILWAYS	09/1995	100	-	591.3
27	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	RAILWAYS	03/1998	280	-	871.73
28	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	RAILWAYS	04/2000	733	733	1,673.08

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
29	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	RAILWAYS	03/2000	1,049.69	3156.32	3,598.21
30	GADWAL - RAICHUR (NL), SCR	RAILWAYS	04/1998	92.63	-	303.2
31	JIND-SONEPAT (NL), NR	RAILWAYS	01/2004	238.56	-	588.78
32	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	RAILWAYS	04/2003	727.56	727.56	2,519.8
33	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR	RAILWAYS	04/2002	921	-	1,473.59
34	PATNA GANGA BRIDGE (NL), ECR	RAILWAYS	04/2001	624.47	-	2,252.44
35	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	RAILWAYS	01/2004	915.7	-	3,045.85
36	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	ROAD TRANSPORT AND HIGHWAYS	12/2003	157.47	157.47	267.6
37	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06	ROAD TRANSPORT AND HIGHWAYS	12/2003	155	-	191.7
38	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31C	ROAD TRANSPORT AND HIGHWAYS	12/2003	230	-	251.5
39	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	ROAD TRANSPORT AND HIGHWAYS	12/2003	280	-	366.1
40	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	ROAD TRANSPORT AND HIGHWAYS	12/2003	155.04	-	173.8
41	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	ROAD TRANSPORT AND HIGHWAYS	12/2003	200	-	207.2
42	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	195	-	280.2

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
43	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	237.8	-	321.4
44	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	332.94	-	525.8
45	KOTA BYPASS,RJ-4, NH-76 (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	275	-	285.3
46	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	251.03	-	384.7
47	ADRIYALA SHAFT PROJECT	COAL	12/2009	212.34	1228.39	1,228.77
48	EXPANSION OF IISCO STEEL PLANT	STEEL	06/2008	14,443	-	16,340.7
49	DEVELOPMENT OF B-193 CLUSTER FIELDS	PETROLEUM	06/2007	3,248.78	5633.44	5,867.78
50	ASSAM GAS CRACKER PROJECT	PETROCHEMICALS	04/2006	5,460.61	-	7,924.14
51	KISHANGANGA HEP	POWER	07/2007	3,642.04	3642.04	3,644.34
52	WESTERN REGION STRENGTHENING SCHEME-V	POWER	12/2007	477.69	-	495.59
53	BARH STPP STAGE -II	POWER	02/2008	7,341.04	-	7,902
54	TRIPURA GAS BASED POWER PROJECT	POWER	07/2009	421.01	623.44	833.58
55	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	POWER	01/2011	368.72	-	656.12
56	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	RAILWAYS	04/1996	332.92	332.92	468.91

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
57	BHOPAL BINA 3D LINE DOUBLING	RAILWAYS	09/2007	687.2	-	798.47
58	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	RAILWAYS	09/2007	404.19	-	442.35
59	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	RAILWAYS	09/2006	343.17	-	806.89
60	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	RAILWAYS	12/2006	170	-	417.7
61	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	RAILWAYS	09/2006	200	-	204.17
62	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	RAILWAYS	04/2006	325	-	374.71
63	TAMLUK DIGHA, LINE DOUBLING (SER)	RAILWAYS	03/1984	293.97	-	462.27
64	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	RAILWAYS	04/2007	482	-	606.09
65	SURATPURA - HANUMANGARH - SRIGANGANAGAR GAUGE CONVERSION (NWR)	RAILWAYS	04/2008	516.23	-	570.8
66	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	RAILWAYS	04/1999	207.52	-	215.45
67	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	RAILWAYS	04/2006	117.36	196.95	198.66
68	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	RAILWAYS	04/1996	1,676.31	-	4,452.04
69	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	RAILWAYS	04/1994	320.66	-	458.16
70	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR	RAILWAYS	04/2013	456	-	557.65

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
71	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	RAILWAYS	04/2010	739.65	-	790.03
72	SAKRI-HASANPUR ROAD (NL)	RAILWAYS	04/1999	175.69	-	248.56
73	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	RAILWAYS	04/1999	198.68	-	268.22
74	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	RAILWAYS	04/1999	271.24	-	462.38
75	NEW BG LINE FROM DUDHNOI-MENDIPATAR	RAILWAYS	04/1999	175.43	-	240.2
76	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	RAILWAYS	04/1999	895	-	994.65
77	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	RAILWAYS	04/2007	247	-	590.71
78	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI	RAILWAYS	04/1999	523.17	-	1,038.3
79	PEN ROHA DOUBLING	RAILWAYS	04/2007	98.74	-	214.24
80	PANVEL PEN DOUBLING	RAILWAYS	04/2006	96.16	-	232.37
81	MUNIRABAD (GINGERA) -RAICHUR NL	RAILWAYS	04/2007	179.65	-	295.46
82	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI	RAILWAYS	04/1999	460.94	-	804.2
83	JHARSUGUDA-RENGALI DOUBLING	RAILWAYS	03/2006	201	-	218.68
84	NALBARI TO BIJNI (AS-8)	ROAD TRANSPORT AND HIGHWAYS	12/2003	200	-	281.6

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
85	GUWHATI TO NALBARI (AS-4)	ROAD TRANSPORT AND HIGHWAYS	12/2003	175.96	-	286.7
86	NAGAON TO DHARAMTUL (AS-2)	ROAD TRANSPORT AND HIGHWAYS	12/2003	264.72	-	315.7
87	SONAPUR TO GUWAHTI (AS-3)	ROAD TRANSPORT AND HIGHWAYS	12/2003	245	-	491.2
88	GUWAHATI TO NALBARI (AS-5)	ROAD TRANSPORT AND HIGHWAYS	12/2003	198.16	-	341
89	NALBARI TO BIJNI (AS-6)	ROAD TRANSPORT AND HIGHWAYS	12/2003	225	-	276.4
90	NALBARI T BIJNI (AS-7)	ROAD TRANSPORT AND HIGHWAYS	12/2003	208	230	334.1
91	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	ROAD TRANSPORT AND HIGHWAYS	12/2003	160	-	211.7
92	DHARAMTUL TO SONAPUR (AS-19)	ROAD TRANSPORT AND HIGHWAYS	12/2003	200	-	288.8
93	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	ROAD TRANSPORT AND HIGHWAYS	03/2005	557	-	1,123
94	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	ROAD TRANSPORT AND HIGHWAYS	12/2003	232.45	-	317.2
95	DELHI/ HARYANA BORDER TO ROHTAK	ROAD TRANSPORT AND HIGHWAYS	04/2007	486	-	666.4
96	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	ROAD TRANSPORT AND HIGHWAYS	03/2005	940	-	1,601
97	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	ROAD TRANSPORT AND HIGHWAYS	03/2010	1,509.1	-	2,613
98	PUNE-SHOLAPUR, PKG1	ROAD TRANSPORT AND HIGHWAYS	11/2009	1,110	-	1,826

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
99	KISHANGARH-AJMER-BEAWER	ROAD TRANSPORT AND HIGHWAYS	11/2009	795	-	1,132
100	CHENNAI-TADA(SIX LANE)	ROAD TRANSPORT AND HIGHWAYS	04/2009	353.37	-	446.2
101	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	ROAD TRANSPORT AND HIGHWAYS	02/2009	1,693.75	-	2,762
102	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15)	ROAD TRANSPORT AND HIGHWAYS	05/2009	572.3	-	886.9
103	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	ROAD TRANSPORT AND HIGHWAYS	05/2009	1,108	-	3,466
104	JAIPUR-TONK-DEOLI	ROAD TRANSPORT AND HIGHWAYS	06/2010	792.06	-	1,983
105	TALEGAON-AMRAVATI	ROAD TRANSPORT AND HIGHWAYS	11/2009	567	-	1,377
106	HAZARIBAGH-RANCHI	ROAD TRANSPORT AND HIGHWAYS	08/2010	625.07	-	995.9
107	ARMUR TO KADLOOR YELLAREDDY	ROAD TRANSPORT AND HIGHWAYS	02/2010	390.56	-	631.7
108	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	ROAD TRANSPORT AND HIGHWAYS	09/2010	852	-	899.7
109	KUNDUPUR-SURATHKAL & MANGLORE	ROAD TRANSPORT AND HIGHWAYS	09/2010	671	-	1,260
110	AMRITSAR-PATHANKOT	ROAD TRANSPORT AND HIGHWAYS	05/2010	705	-	2,208
111	DEOLI-KOTA	ROAD TRANSPORT AND HIGHWAYS	01/2011	593	-	759.9
112	PANIPAT-ROHTAK	ROAD TRANSPORT AND HIGHWAYS	04/2011	807	-	1,209.43

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
113	DEVIHALLI-HASSAN	ROAD TRANSPORT AND HIGHWAYS	12/2010	453	-	801.4
114	MURADABAD-BAREILY	ROAD TRANSPORT AND HIGHWAYS	04/2010	1,267	-	2,415
115	4 LANING OF NAGPUR-BETUL	ROAD TRANSPORT AND HIGHWAYS	02/2011	2,498.76	-	2,786
116	BELGAUM-DHARWAD(NH-4)	ROAD TRANSPORT AND HIGHWAYS	12/2010	480	-	664.6
117	INDORE-DEWAS(NH-3)	ROAD TRANSPORT AND HIGHWAYS	11/2010	325	-	609.5
118	2 LANNING OF MOKAMA-MUNGER	ROAD TRANSPORT AND HIGHWAYS	05/2011	351.54	-	396.4
119	4 LANNING OF AHMEDABAD TO GODHARA	ROAD TRANSPORT AND HIGHWAYS	12/2010	1,008.5	-	1,381
120	4 LANNING OF GODHARA TO GUJARAT/MP BORDER	ROAD TRANSPORT AND HIGHWAYS	03/2011	785.5	-	940.5
121	ROHTAK-BAWAL	ROAD TRANSPORT AND HIGHWAYS	05/2011	650	-	1,178
122	GHAZIABAD-ALIGARH NH-91	ROAD TRANSPORT AND HIGHWAYS	02/2011	1,141	-	2,157
123	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	ROAD TRANSPORT AND HIGHWAYS	09/2011	1,250	-	1,321
124	SAMAIKHALI - GANDHIDHAM	ROAD TRANSPORT AND HIGHWAYS	09/2010	805.39	-	841.9
125	JORBAT - BARAPANI	ROAD TRANSPORT AND HIGHWAYS	01/2011	536	-	746.9
126	2-LANNING OF SHILONG BYPASS	ROAD TRANSPORT AND HIGHWAYS	02/2011	226	-	282.3

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
127	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	ROAD TRANSPORT AND HIGHWAYS	11/2011	1,535	-	2,188
128	2-LANNING WITH PS KHAGARIA-PURNEA	ROAD TRANSPORT AND HIGHWAYS	05/2011	664	-	769.5
129	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	ROAD TRANSPORT AND HIGHWAYS	09/2011	574	-	982.4
130	2-LANNING WITH PS MOTIHARI-RAXAUL	ROAD TRANSPORT AND HIGHWAYS	10/2011	375.09	-	406.6
131	4-LANNING OF CHAPRA-HAJIPUR	ROAD TRANSPORT AND HIGHWAYS	01/2011	575	-	825.4
132	2 LANNING OF MUZAFFARPUR - SONBARSA	ROAD TRANSPORT AND HIGHWAYS	05/2011	511.54	-	1,179
133	4-LANING OF BARHI-HAZARIBAGH	ROAD TRANSPORT AND HIGHWAYS	02/2012	398	-	461.9
134	BHUBANESWAR TO PURI	ROAD TRANSPORT AND HIGHWAYS	03/2011	500.29	-	632.8
135	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER	ROAD TRANSPORT AND HIGHWAYS	11/2011	909	-	974.3
136	JAIPUR-REENGUS	ROAD TRANSPORT AND HIGHWAYS	08/2010	267.81	-	698.2
137	4-LANING OF FARAKA-RAIGANJ	ROAD TRANSPORT AND HIGHWAYS	02/2011	1,078.84	-	1,906
138	4-LANING OF BRAHAMPORE-FARAKA	ROAD TRANSPORT AND HIGHWAYS	02/2011	998.79	-	1,597
139	6-LANING OF DHANKUNI-KHARAGPUR SECTION	ROAD TRANSPORT AND HIGHWAYS	04/2012	1,396.18	-	1,760
140	KRISHNANAGAR-BERHAMPUR	ROAD TRANSPORT AND HIGHWAYS	02/2012	702.16	-	719.2

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
141	FOUR LANNING OF WALAYAR-VADAKKANANCHERRY SECTION	ROAD TRANSPORT AND HIGHWAYS	04/2011	682	-	729.4
142	2 LANING WITH PS AGRA ALIGARH	ROAD TRANSPORT AND HIGHWAYS	10/2012	250.5	-	363.1
143	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	SHIPPING AND PORTS	03/2007	245.67	298.17	371.18

Details of Projects Without Original Date of Commissioning

(September 2014)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>PETROLEUM</u>								
1	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL, MAHARASHTRA	12/2009	1,584.00 -	1,584.00	1,006.92	- -	08/2015	-	0/12
	Total		1,584.00 -	1,584.00	1,006.92				0/12
	<u>POWER</u>								
2	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]NEEPCO, TRIPURA	07/2012	296.87 -	296.87	279.18	- 03/2015	03/2015	0(R3)	0/17
	Total		296.87 -	296.87	279.18				0/17
	<u>RAILWAYS</u>								
3	MUNEERABAD-MAHABOONAGAR(NL), SCR - [220100205]SCR, MULTI STATE	04/1997	218.24 236.41	645.00	305.66	- -	12/2014	-	0/0
4	KANPUR-KASGANJ-MATHURA(GC), NER - [220100197]NER, UTTAR PRADESH	03/1997	677.97 1,062.36	1,651.54	1,604.79	- -	03/2015	-	0/0
5	GULBARGA-BIDAR, SCR(NL) - [220100254]SCR, KARNATAKA	02/1998	242.42 369.70	844.00	621.23	- 05/2009	03/2015	70(R1)	0/0
6	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER, UTTAR PRADESH	03/2002	863.23 -	1,072.51	874.58	- -	03/2015	-	0/0
7	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]NEFR, ASSAM	01/2004	915.70 -	3,019.17	3,045.85	- -	03/2015	-	0/0
8	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR, TAMIL NADU	09/2006	343.17 -	914.98	806.89	- -	03/2015	-	0/0
9	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONG WITH ELECTRIF - [N22000202]SR, TAMIL NADU	04/2007	247.00 -	951.24	590.71	- -	03/2015	-	0/0
10	PEN ROHA DOUBLING - [N22000254]CR, MULTI STATE	04/2007	98.74 -	203.00	214.24	- -	03/2015	-	0/0
11	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NEFR, ASSAM	09/2006	200.00 -	430.33	204.17	- -	03/2017	-	0/0
12	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NEFR, WEST BENGAL	04/2011	209.77 -	209.77	75.14	- -	03/2017	-	0/0
13	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NEFR, WEST BENGAL	04/2012	283.55 -	283.55	8.02	- -	03/2017	-	0/0
14	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NEFR, ASSAM	04/2011	312.12 -	312.12	107.90	- -	03/2017	-	0/0

(September 2014)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
15	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 -	315.13	1.61	- -	12/2017	-	0/0
16	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	2,050.00	188.72	- -	11/2014	-	0/0
	Total		6,920.11 -	12,902.34	8,649.51				0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
17	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,KARNATAKA	12/2010	480.00 -	480.00	664.60	- -	10/2014	-	2/2
18	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,KARNATAKA	09/2010	671.00 -	671.00	1,260.00	- -	06/2015	-	2/3
	Total		1,151.00 -	1,151.00	1,924.60				4/5
	Grand Total		9,951.98	15,934.21	11,860.21				4/34

Details of Projects Without Date of Commissioning

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>CIVIL AVIATION</u>				
1	GAGAN PROJECT - [N04000065]AAI,MULTI STATE	09/2008	626.00 -	06/2013 -	06/2013
	Total		626.00 -		
	<u>COAL</u>				
2	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,UTTAR PRADESH	06/2011	789.88 -	03/2013 -	03/2014
3	MURAI DIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	04/2014 -	04/2014
4	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	03/2012 -	-
5	JALLARAM SHAFT PROJECT - [N06000025]SCCL,TELANGANA	09/2007	467.78 -	03/2013 -	-
	Total		1,846.57 -		
	<u>PETROCHEMICALS</u>				
6	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,ASSAM	04/2006	5,460.61 -	04/2012 -	-
	Total		5,460.61 -		
	<u>PETROLEUM</u>				
7	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	- -	-
8	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	- -	-
9	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,HARYANA	11/2007	281.07 -	10/2010 -	-
10	DBNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,MULTI STATE	12/2009	540.92 -	06/2011 07/2012	-
	Total		1,704.82 -		
	<u>POWER</u>				
11	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	09/2008 -	03/2013
12	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,MULTI STATE	02/2009	184.19 -	11/2011 -	06/2014
13	RAMPUR HEP(412 MW) - [N18000024]SJVN, HIMACHAL PRADESH	01/2007	2,047.03 -	03/2012 -	-
14	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	02/2012 -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
15	765 KV POOLING STATION AND NETWORK WITH DVC AND MAITHOB RBC - [N18000069]PGCIL,MULTI STATE	08/2008	7,075.33 -	08/2012 -	-
16	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNAM OF ANDHRA PRADESH(PGCIL) - [N18000111]PGCIL,MULTI STATE	08/2011	1,637.34 -	08/2014 -	-
17	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 -	08/2014 -	-
18	TRANSMISSION SYS ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1 - [N18000121]PGCIL,MULTI STATE	02/2012	324.33 -	08/2014 -	-
19	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,BIHAR	12/2011	901.77 -	08/2014 -	-
20	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,KARNATAKA	03/2005	1,007.16 -	12/2007 12/2009	-
21	SYSTEM STRENGTHENING -XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	06/2012 -	-
22	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,ANDHRA PRADESH	03/2012	206.44 -	06/2014 -	-
	Total		16,102.84 -		
	<u>RAILWAYS</u>				
23	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	07/2008
24	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87 -	- 03/2010	03/2010
25	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	02/2012
26	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	02/2009 -	03/2012
27	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N22000052]WS&PU,BIHAR	04/2003	98.74 224.51	- -	03/2012
28	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,BIHAR	03/2005	470.09 1,417.97	- -	03/2012
29	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 03/2012	12/2012
30	GHUTIASARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	611.03 -	12/2011 11/2013	11/2013
31	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- -	12/2013
32	PEDAPALI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 -	- -	02/2014
33	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2014
34	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	02/2009 02/2009	08/2014
35	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL, ODISHA	04/2000	133.41 207.00	03/2009 03/2009	08/2014
36	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-
37	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	- 09/2009	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
38	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-
39	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-
40	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	03/2010 -	-
41	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR(221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	- -	-
42	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 -	- 03/2010	-
43	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 663.01	06/1999 -	-
44	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NEFR,WEST BENGAL	04/1983	36.80 274.41	- -	-
45	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	12/2011 12/2010	-
46	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	- -	-
47	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 -	- -	-
48	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	- -	-
49	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,038.00	03/1998 -	-
50	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	37.68 -	07/2012 -	-
51	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-
52	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	- -	-
53	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	2,957.21 -	07/2005 -	-
54	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	05/2008 -	-
55	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 335.77	03/2012 -	-
56	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,BIHAR	09/2001	492.98 -	12/2010 -	-
57	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	- -	-
58	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	744.71 -	- -	-
59	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-
60	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-
61	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 -	- -	-
62	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE	03/1998	280.00 -	- -	-
63	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
64	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 3,156.32	12/2006 -	-
65	GADWAL - RAICHUR (NL), SCR - [220100270]SCR, MULTI STATE	04/1998	92.63 -	02/2011 02/2011	-
66	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	- 12/2009	-
67	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER, MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-
68	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR, KARNATAKA	02/1999	138.00 -	- -	-
69	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	03/2005 12/2008	-
70	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR, ODISHA	04/1994	470.21 -	- -	-
71	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR, BIHAR	04/2003	528.65 -	- -	-
72	KOSI BRIDGE (NL), ECR - [220100304]ECR, BIHAR	04/2002	322.95 -	03/2012 -	-
73	KODERMA-TILAIYA (NL), ECR - [220100305]ECR, JHARKHAND	04/2002	459.91 -	- -	-
74	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR, BIHAR	04/2001	406.92 -	- -	-
75	RAMGANJMUNDI-BHOPAL (NL), WCR - [220100314]WCR, MADHYA PRADESH	04/2001	470.92 727.13	- -	-
76	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER, BIHAR	04/2003	218.19 -	- -	-
77	HATHUA-BHATNI (N L) (NER) - [220100319]NER, MULTI STATE	04/2005	230.03 -	- -	-
78	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR, ODISHA	04/2005	810.78 -	- -	-
79	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR, BIHAR	04/1996	332.92 332.92	03/2012 -	-
80	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N220000028]MRTP, TAMIL NADU	04/2006	495.74 -	06/2013 06/2013	-
81	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N220000032]SCR, TELANGANA	04/2006	378.56 -	- -	-
82	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' - AGASTIYAMPALLI - [N220000079]SR, TAMIL NADU	09/2007	404.19 -	- -	-
83	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N220000082]NEFR, MULTI STATE	12/2006	170.00 -	03/2011 -	-
84	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N220000084]SR, TAMIL NADU	09/2006	125.00 -	- -	-
85	TIDIVANAM-NAGARI (NL) - [N220000085]SR, TAMIL NADU	09/2006	456.00 -	- -	-
86	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N220000087]NEFR, BIHAR	09/2006	300.00 -	- -	-
87	BARDHAMAN-KATWA (GC) - [N220000091]ER, WEST BENGAL	04/2007	1,106.62 -	12/2010 -	-
88	TAMLUK DIGHA, LINE DOUBLING (SER) - [N220000097]SER, WEST BENGAL	03/1984	293.97 -	06/2005 07/2011	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
89	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,BIHAR	04/2008	282.92 -	- -	-
90	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	03/2014 -	-
91	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 -	03/2014 -	-
92	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	-
93	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER,WEST BENGAL	04/2009	259.51 -	12/2011 -	-
94	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER,WEST BENGAL	04/2004	293.74 -	12/2010 -	-
95	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 -	12/2012 -	-
96	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-
97	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	03/2013 -	-
98	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	03/2014 -	-
99	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	-
100	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-
101	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
102	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	-
103	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	-
104	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	- -	-
105	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	- -	-
106	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
107	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	- -	-
108	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-
109	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	- -	-
110	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	- -	-
111	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	- -	-
112	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-
113	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
114	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT	04/2013	1,266.89 -	- -	-
115	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	- -	-
116	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	- -	-
117	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2012	2,082.75 -	- -	-
118	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	-
119	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
120	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
121	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	- -	-
122	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	- -	-
123	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	- -	-
124	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	- -	-
125	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	- -	-
126	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	- -	-
127	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- -	-
128	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 -	- -	-
129	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	- -	-
130	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	- -	-
131	NAWADA-LAXMIPUR (NL) - [N22000167]SER,BIHAR	04/2008	620.57 -	- -	-
132	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-
133	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-
134	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-
135	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-
136	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-
137	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-
138	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-
139	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
140	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-
141	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-
142	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-
143	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
144	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-
145	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-
146	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-
147	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NEFR,MULTI STATE	04/2013	1,798.00 -	- -	-
148	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	- -	-
149	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-
150	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
151	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-
152	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1999	271.24 -	- -	-
153	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	- -	-
154	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-
155	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
156	NEW BG LINE FROM DUDHNOI-MENDIPATAR - [N22000192]NEFR,MULTI STATE	04/1999	175.43 -	- -	-
157	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NEFR,WEST BENGAL	04/2010	221.42 -	- -	-
158	AGARTALA-AKHAURA NL - [N22000195]NEFR,TRIPURA	04/2012	252.00 -	- -	-
159	DIMAPUR-TIZIT NL - [N22000196]NEFR,NAGALAND	04/2013	4,274.00 -	- -	-
160	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
161	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-
162	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-
163	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-
164	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NEFR,MEGHALAYA	04/2010	4,083.02 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
165	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NEFR,MULTI STATE	04/2010	242.22 -	- -	-
166	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NEFR,MULTI STATE	04/2010	241.52 -	- -	-
167	MURKONGSELEK-PASIGHAT NL - [N22000208]NEFR,MULTI STATE	04/2011	165.82 -	- -	-
168	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NEFR,MULTI STATE	04/1999	523.17 -	- -	-
169	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NEFR,ASSAM	04/2012	246.07 -	- -	-
170	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-
171	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-
172	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1999	406.99 -	- -	-
173	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-
174	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-
175	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-
176	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-
177	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-
178	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-
179	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-
180	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-
181	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-
182	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRACHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-
183	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-
184	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-
185	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	- -	-
186	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-
187	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
188	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-
189	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-
190	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-
191	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-
192	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-
193	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-
194	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-
195	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-
196	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	182.06 -	- -	-
197	SANTOSHPUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-
198	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-
199	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-
200	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	96.16 -	- -	-
201	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-
202	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-
203	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	- -	-
204	MANUGURU-RAMAGUNDAM - [N22000259]SCOR,TELANGANA	04/2013	1,112.00 -	- -	-
205	KONDAPALLI-PENUBALLI - [N22000260]SCOR,MULTI STATE	04/2013	723.00 -	- -	-
206	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCOR,MULTI STATE	04/2012	1,054.35 -	- -	-
207	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCOR,MULTI STATE	04/2008	184.26 -	- -	-
208	BHADRACHALAM-KOVVUR - [N22000264]SCOR,MULTI STATE	04/2012	923.23 -	- -	-
209	GUDUR-DURGARA JAPATNAM - [N22000265]SCOR,ANDHRA PRADESH	04/2011	283.54 -	- -	-
210	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-
211	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
212	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-
213	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-
214	DELHI-SOHNANUHIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-
215	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-
216	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-
217	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-
218	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	-
219	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-
220	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-
221	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	- -	-
222	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-
223	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-
224	CUMBUM-PRODDATUR - [N22000282]SCOR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
225	MUDKHED-PARBHANI - [N22000283]SCOR,MAHARASHTRA	04/2011	390.60 -	- -	-
226	NADIKUDE-SRI KALAHASTI - [N22000286]SCOR,ANDHRA PRADESH	04/2011	1,313.48 -	- -	-
227	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCOR,MULTI STATE	04/2010	337.49 -	- -	-
228	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
229	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-
230	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-
231	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-
232	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-
233	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-
234	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-
235	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-
236	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	- -	-
237	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
238	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	- -	-
239	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	-
240	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-
241	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-
242	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	01/1999 -	-
243	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 -	-
244	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-
245	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	01/1999 -	-
246	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-
247	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 -	- -	-
248	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 -	- -	-
249	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	- -	-
250	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 -	- -	-
251	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	- -	-
252	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-
253	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR,TAMIL NADU	04/2011	190.10 -	- -	-
254	HOSADURGA - CHICKJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA	04/2010	203.40 -	- -	-
	Total		111,892.81 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
255	PUNE-SHOLAPUR,PKG1 - [N24000127]NHAI,MAHARASHTRA	11/2009	1,110.00 -	05/2012 -	03/2012
256	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	07/2012 -	07/2012
257	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	12/2012 -	12/2012
258	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	01/2013 -	01/2013
259	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	02/2013 -	02/2013
260	DEVIHALLI-HASSAN - [N24000152]NHAI,KARNATAKA	12/2010	453.00 -	- -	05/2013
261	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	05/2013

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
262	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI, TELANGANA	02/2010	390.56 -	02/2012 -	06/2013
263	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI, GUJARAT	12/2010	1,008.50 -	06/2013 -	06/2013
264	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI, GUJARAT	03/2011	785.50 -	08/2013 -	08/2013
265	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI, TAMIL NADU	09/2010	1,655.00 -	09/2013 -	09/2013
266	TALEGAON-AMRAVATI - [N24000140]NHAI, MAHARASHTRA	11/2009	567.00 -	11/2013 -	11/2013
267	ROHTAK-BAWAL - [N24000169]NHAI, HARYANA	05/2011	650.00 -	11/2013 -	11/2013
268	2 LANING OF MUZAFFARPUR - SONBARSA - [N24000174]NHAI, BIHAR	05/2011	511.54 -	11/2013 -	11/2013
269	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI, MEGHALAYA	02/2011	226.00 -	02/2014 -	02/2014
270	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, BIHAR	05/2011	664.00 -	02/2014 -	02/2014
271	2LANING WITH PS GOPALGANJ-CHAPPRA - [N24000190]NHAI, BIHAR	12/2011	325.00 -	05/2014 -	05/2014
272	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI, KARNATAKA	11/2010	680.00 -	- -	07/2014
273	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI, BIHAR	12/2003	300.00 -	10/2008 -	-
274	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, WEST BENGAL	12/2003	225.00 -	07/2008 -	-
275	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, ASSAM	12/2003	200.00 -	06/2008 -	-
276	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI, KARNATAKA	09/2010	946.00 -	- -	-
277	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI, MAHARASHTRA	05/2013	1,348.20 -	- -	-
278	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI, ANDHRA PRADESH	09/2013	606.00 -	- -	-
279	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI, TELANGANA	04/2014	1,123.17 -	- -	-
	Total		16,750.95 -		
	<u>SHIPPING AND PORTS</u>				
280	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST, ODISHA	12/2005	154.84 253.36	- 01/2009	12/2010
281	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL, KERALA	03/2007	245.67 298.17	04/2009 11/2009	02/2011
282	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY VESSELS - [N25000014]SHIPP., MAHARASHTRA	10/2007	359.44 -	04/2011 11/2011	11/2011
283	MODIFICATION & STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST, GUJARAT	06/2010	277.00 -	03/2012 -	03/2012
284	ACQUISITION OF TWO NOS. OF 3060 DWT - [N25000043]SHIPP., MAHARASHTRA	04/2009	277.03 280.00	12/2011 10/2012	10/2012

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
285	MECHANIZATION OF COAL HANDLING FACILITIES TO 200000 DWT VESSELS ON DBFOT BASIS - [N25000049]PORT TRUST,ANDHRA PRADESH	02/2010	444.10 -	06/2010 -	11/2012
286	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST - [N25000037]PORT TRUST,GUJARAT	04/2005	882.00 -	02/2011 -	12/2012
287	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,GUJARAT	12/2005	702.00 -	03/2011 -	03/2013
288	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST,GUJARAT	02/2011	830.00 -	05/2013 -	05/2013
289	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,MULTI STATE	07/2011	220.49 -	01/2013 06/2013	06/2013
290	ACQUISITION OF 4 NOS OF 82000 DWT KAMSAVMAX BULK CARRIERS FROM M/S JIANGSU EASTERN HEAVY INDUSTRIES - [N25000051]SHIPP.,MAHARASHTRA	08/2010	612.72 532.83	12/2012 11/2013	11/2013
291	ACQUISITION OF THREE(3) NOS OF 6500TEU CELLULAR CONTAINER VESSELS FROM M/S STX SHIPBUILDING CO. LTD. - [N25000052]SHIPP.,MAHARASHTRA	10/2010	1,028.10 1,012.23	12/2013 11/2013	11/2013
292	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 309.00	03/2006 06/2014	06/2014
293	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY - [N25000062]SHIPP.,MULTI STATE	01/2012	511.87 -	03/2014 08/2014	08/2014
294	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 11/2010	-
295	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL - [N25000003]PORT TRUST,MAHARASHTRA	10/2005	800.00 1,571.60	10/2008 -	-
	Total		9,922.66 -		
	<u>TELECOMMUNICATIONS</u>				
296	SUPPLY INSTALLATION TESTING AND COMMISSIONING OF RURAL WIMAX NETWORK PHASE-II - [N26000100]BSNL,MULTI STATE	07/2010	1,148.19 -	05/2011 -	06/2014
	Total		1,148.19 -		
	<u>URBAN DEVELOPMENT</u>				
297	C/O MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	10/2012 -	09/2013
298	C/O MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB - [N28000070]CPWD,PUNJAB	08/2005	191.24 -	08/2007 -	12/2010
299	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI - [N28000064]CPWD,DELHI	01/2010	162.90 -	07/2012 -	07/2012
300	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA	05/2006	6,395.00 -	06/2011 -	03/2013
301	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI - [N28000048]CPWD,MAHARASHTRA	11/2006	114.18 173.08	04/2009 -	-
	Total		7,028.55 -		
	<u>WATER RESOURCES</u>				

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
302	PAGLADIYA DAM PROJECT - [300100001]MOWR,ASSAM	01/2001	542.90 -	12/2007 -	12/2012
	Total		542.90 -		
	Grand Total		173,026.90		

Details of Projects Ahead of Schedule w.r.t. Original Schedule

							(September 2014)
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
1	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]	2/2011	452.00 -	452.00	309.21	03/2015 -	02/2015
	Total		452.00 -	452.00	309.21		
	<u>POWER</u>						
2	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]	9/2012	1,508.74 -	1,508.74	402.08	06/2016 -	12/2015
	Total		1,508.74 -	1,508.74	402.08		
	<u>PETROLEUM</u>						
3	KOTA JOBNER PIPELINE PROJECT - [N16000170]	4/2011	276.26 -	276.27	174.81	12/2015 -	03/2015
4	LPG MARKETING TERMINAL, PARADIP - [N16000174]	7/2009	158.91 -	158.91	113.85	03/2015 -	02/2015
5	RESITEMENT OF BILASPUR AND BISRAPUR DEPOTS TO KORBA (CHATTISGARH) - [N16000186]	1/2011	141.86 219.08	219.08	93.99	09/2016 -	12/2015
	Total		577.03 -	654.26	382.65		
	<u>POWER</u>						
6	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]	9/2012	1,935.35	1,935.35	-	12/2014 -	11/2014
7	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154]	10/2013	1,315.90 -	1,315.90	-	11/2016 -	03/2016
8	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52	1,364.52	-	05/2016 -	04/2016
	Total		4,615.77 -	4,615.77	.00		
	Grand Total		7,153.54	7,230.77	1,093.94		

Details of On Schedule Projects w.r.t. Original Schedule

(September 2014)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
1	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]	6/2011	746.04 -	535.10	273.52	03/2015 -	03/2015
2	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]	12/2009	1,352.04 -	1,143.54	664.83	03/2016 03/2016	03/2016
3	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.00 -	490.10	183.63	03/2017 -	03/2017
4	BATURA OCP (2.0 MTY) - [N06000049]	9/2008	203.82 -	203.82	-	03/2015 -	03/2015
5	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	94.90	03/2016 -	03/2016
6	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	43.25	03/2018 -	03/2018
7	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]	4/2012	258.56 -	258.56	60.25	03/2016 -	03/2016
8	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	97.05	03/2020 -	03/2020
9	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	6.84	03/2021 -	03/2021
10	KULDA EXPN OC. (5.00 MTY) - [N06000115]	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
11	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]	5/2014	337.66 -	337.66	-	03/2019 -	03/2019
12	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	-	03/2026 -	03/2026
13	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]	5/2014	479.15 -	479.15	-	03/2019 -	03/2019
14	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	22.10	03/2020 -	03/2020
15	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]	8/2012	1,055.05 -	1,055.05	30.31	03/2018 -	03/2018
16	KAPURIA UG(PSLW) - [N06000108]	8/2011	988.35 -	988.35	6.84	04/2017 -	04/2017
17	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.33 -	610.33	-	03/2022 -	03/2022
18	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.14 -	430.14	68.08	03/2016 -	03/2016
19	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	7/2011	162.76 -	162.76	2.48	03/2015 -	03/2015
20	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]	12/2009	510.85 -	510.85	223.57	03/2016 -	03/2016
21	RKP OCP PHASE-I - [N06000079]	3/2010	209.78 -	209.78	68.51	03/2015 -	03/2015
22	PELMA OCP(10.00MTY) - [N06000045]	7/2008	448.32 -	448.32	0.46	03/2015 -	03/2015

(September 2014)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		15,188.23	14,816.89	1,846.62		
			-				
	<u>PETROLEUM</u>						
23	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]	3/2012	5,608.40	5,608.40	2,805.04	05/2015	05/2015
24	MOUNDED BULLET PROJECT AT CPCL - [N16000154]	12/2012	279.00	279.00	95.32	12/2014	12/2014
25	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]	12/2012	3,513.07	3,513.07	0.27	02/2016	02/2016
26	KG BASIN PIPELINE REPLACEMENT PROJECT - [N16000190]	7/2014	762.00	762.00	-	01/2017	01/2017
27	GUJARAT REGION PIPELINE REPLACEMENT PROJECT - [N16000189]	7/2014	716.00	716.00	-	01/2017	01/2017
28	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	6/2014	5,706.47	5,706.47	-	05/2017	05/2017
29	RESID UPGRADE PROJECT - [N16000184]	2/2011	3,110.36	3,110.36	242.84	11/2015	11/2015
30	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]	3/2014	2,476.82	2,476.82	-	12/2018	12/2018
31	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS - [N16000181]	3/2013	2,913.10	2,910.30	9.50	05/2016	05/2016
32	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]	2/2014	163.88	163.88	3.82	07/2016	07/2016
33	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00	3,150.00	92.49	09/2017	09/2017
34	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]	4/2013	480.00	480.00	3.02	02/2016	02/2016
35	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]	3/2014	3,076.00	3,076.00	42.24	09/2017	09/2017
36	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]	4/2013	284.82	284.82	-	04/2015	04/2015
37	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	5/2013	4,124.35	4,124.35	-	04/2016	04/2016
38	LPG TERMINAL AT KOCHI - [N16000171]	12/2012	607.06	607.06	47.38	01/2016	01/2016
39	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]	3/2013	1,138.50	1,138.50	145.86	04/2015	04/2015
40	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]	9/2011	202.25	160.16	36.33	07/2016	07/2016
41	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]	8/2011	586.00	586.00	198.47	08/2015	08/2015
42	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	3/2012	14,225.00	16,504.00	3,483.53	05/2016	05/2016
43	REWARI KANPUR PIPELINE PROJECT - [N16000145]	2/2012	1,210.64	1,210.64	732.58	11/2015	11/2015
44	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	2/2012	666.00	701.00	312.24	11/2015	11/2015
	Total		54,999.72	57,268.83	8,250.93		
			-				

(September 2014)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	POWER						
45	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]	2/2012	1,310.85 -	1,310.85	-	02/2015 -	02/2015
46	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]	9/2012	803.34 -	803.34	379.39	03/2015 -	03/2015
47	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139]	1/2013	182.80 -	182.80	76.33	10/2014 -	10/2014
48	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]	10/2014	8,112.12 -	8,112.12	-	04/2020 -	04/2020
49	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	2/2014	196.58 -	196.58	-	02/2016 -	02/2016
50	TRANS. SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]	8/2014	188.75 -	188.75	-	02/2017 -	02/2017
51	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]	2/2014	243.53 -	243.53	-	08/2016 -	08/2016
52	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	2/2014	908.08 -	908.08	-	06/2016 -	06/2016
53	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]	2/2014	539.82 -	539.82	-	06/2016 -	06/2016
54	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]	1/2014	374.63 -	374.63	-	04/2016 -	04/2016
55	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]	9/2013	1,575.30 -	1,575.30	-	05/2016 -	05/2016
56	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]	9/2013	680.69 -	680.69	-	03/2016 -	03/2016
57	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]	6/2012	1,909.24 -	1,909.24	598.63	06/2015 -	06/2015
58	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]	3/2013	2,514.88 -	2,514.88	237.85	12/2015 -	12/2015
59	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	3/2013	514.20 -	514.20	-	06/2015 -	06/2015
60	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]	8/2014	288.49 -	288.49	-	02/2017 -	02/2017
61	TRANS.SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	-	04/2018 -	04/2018
62	TRANS. SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]	6/2014	400.47 -	400.47	-	05/2017 -	05/2017
63	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3&4 - [N18000166]	2/2014	378.71 -	378.71	11.20	10/2016 -	10/2016
64	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]	3/2014	155.57 -	155.57	-	03/2016 -	03/2016
65	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 -	522.29	-	11/2016 -	11/2016
66	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]	5/2014	303.07 -	303.07	-	07/2016 -	07/2016

(September 2014)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
67	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]	5/2014	829.98 -	829.98	-	09/2016 -	09/2016
68	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]	2/2014	167.40 -	167.40	-	12/2015 -	12/2015
69	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]	12/2012	156.04 -	156.04	-	10/2014 -	10/2014
70	VINDHYACHAL STPP STAGE-V - [N18000134]	12/2011	3,180.40 -	3,180.40	1,234.00	08/2015 -	08/2015
71	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]	2/2012	1,927.16 -	1,927.16	-	10/2014 -	10/2014
72	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]	3/2012	198.63 -	198.63	-	09/2014 -	09/2014
73	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]	6/2012	1,263.26 -	1,263.26	-	11/2014 -	11/2014
	Total		34,977.65 -	34,977.65	2,537.40		
	<u>RAILWAYS</u>						
74	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	4/1998	183.23 -	818.29	-	02/2015 -	02/2015
75	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]	4/2010	622.41 -	2,030.50	2.43	02/2019 -	02/2019
76	PLASSEY-JIAGANJ DOUBLING - [N22000220]	4/2011	248.07 -	248.07	26.60	03/2015 -	03/2015
77	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	4/2012	148.77 -	174.69	1.80	12/2016 -	12/2016
78	DELANG-PURI DOUBLING - [N22000320]	3/2011	165.16 -	165.16	106.62	03/2015 -	03/2015
79	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	4/2010	423.66 -	423.66	215.50	03/2017 -	03/2017
80	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	4/2011	299.60 -	299.60	1.10	03/2017 -	03/2017
81	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]	4/2012	714.10 -	714.10	46.02	04/2016 -	04/2016
82	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	1,176.09 -	3,845.60	1.92	02/2020 -	02/2020
83	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	4/2010	3,951.98 -	4,259.48	733.02	03/2016 -	03/2016
84	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	4/2010	2,913.51 -	2,913.51	382.68	03/2016 -	03/2016
85	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	3/2013	4,874.58 -	4,874.58	1,741.00	03/2016 -	03/2016
86	HIMMATNAGAR - UDAIPUR GAUGE CONVERSION (NWR) - [N22000112]	4/2008	829.74 -	829.74	75.09	03/2015 -	03/2015
	Total		16,550.90 -	21,596.98	3,333.78		

(September 2014)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
87	PANIPAT-ROHTAK - [N24000151]	4/2011	807.00 -	807.00	1,209.43	10/2014 -	10/2014
88	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]	2/2013	1,232.00 -	1,232.00	590.90	08/2015 -	08/2015
89	2 LANING WITH PS AGRA ALIGARH - [N24000220]	10/2012	250.50 -	250.50	363.10	10/2014 -	10/2014
90	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	1,928.22	642.90	04/2015 -	04/2015
91	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]	6/2013	1,287.95 -	1,287.95	540.10	11/2015 -	11/2015
92	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]	11/2013	1,916.79 -	1,916.79	273.20	11/2016 -	11/2016
93	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	4/2014	1,266.60 -	1,266.60	-	09/2016 -	09/2016
94	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]	10/2013	283.25 -	283.25	218.70	10/2015 -	10/2015
95	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]	10/2011	1,565.00 -	1,565.00	1,556.00	10/2014 -	10/2014
96	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	150.20	12/2015 -	12/2015
97	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	919.30	09/2015 -	09/2015
98	RANCHI-RARGA-JAMSETHPUR - [N24000215]	12/2012	1,479.00 -	1,479.00	354.70	06/2015 -	06/2015
99	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]	4/2012	1,396.18 -	1,396.18	1,760.00	09/2014 -	09/2014
	Total		17,110.73 -	17,110.73	8,578.53		
	<u>STEEL</u>						
100	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]	11/2012	313.05 -	313.05	135.24	06/2015 -	06/2015
101	REBUILDING OF COB-7 AT BSL - [N12000083]	10/2013	245.67 -	245.67	18.01	05/2016 -	05/2016
102	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]	6/2014	708.91 -	708.91	1.79	04/2016 -	04/2016
103	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT [N12000085]	4/2014	188.93 -	188.93	-	04/2015 -	04/2015
	Total		1,456.56 -	1,456.56	155.04		
	<u>URBAN DEVELOPMENT</u>						
104	DELHI MRTS PHASE-III - [N28000056]	9/2011	38,585.00 -	38,585.00	8,699.49	03/2016 -	03/2016
105	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]	2/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019

(September 2014)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
106	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]	4/2014	332.72 -	332.72	0.08	09/2016 -	09/2016
107	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]	2/2012	171.10 -	171.10	85.60	09/2014 -	09/2014
108	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]	2/2011	241.33 -	241.33	22.43	11/2014 -	11/2014
109	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,219.21	-	07/2017 -	07/2017
110	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]	6/2014	157.84 -	157.84	2.04	03/2017 -	03/2017
	Total		67,112.34 -	67,112.34	8,809.64		
	Grand Total		207,396.13	214,339.98	33,511.94		

Details of Delayed Projects w.r.t. Original and Revised Schedule

						(September 2014)		All Cost/ Expenditure in Rs. crore	
						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticip ated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Antici Pated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00 17,270.00	17,270.00	17,894.00	12/2008 10/2013	11/2014	71	31.12
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 5,677.00	5,677.00	4,723.19	09/2010 03/2015	03/2015	54	62.57
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	5,399.00	12/2015 11/2016	10/2017	22	0
4	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	3,294.00	12/2016 03/2017	05/2018	17	0
	Total		40,442.00 -	46,726.00	31,310.19				
	<u>CIVIL AVIATION</u>								
5	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 335.61	388.53	284.00	05/2012 -	10/2014	29	15.77
6	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	344.28	19.61	03/2014 -	01/2015	10	0
7	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	217.60	0.04	03/2015 -	03/2016	12	0
8	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	309.46	277.91	01/2011 04/2013	12/2016	71	0
	Total		1,206.95 -	1,259.87	581.56				
	<u>COAL</u>								
9	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,TAMIL NADU	10/2004	2,030.78 3,027.59	3,321.86	3,035.56	06/2009 03/2013	10/2014	64	63.58
10	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	5,632.17	03/2012 05/2014	11/2014	32	34.63
11	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]NLC,TAMIL NADU	04/2012	364.75 -	364.75	92.32	10/2014 -	11/2014	1	0
12	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 -	259.40	7.45	03/2012 -	03/2015	36	0
13	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	453.63	105.42	12/2012 -	03/2015	27	0
14	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	144.07	03/2013 -	03/2015	24	0

(September 2014) All Cost/
Expenditure in
Rs. crore

						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
15	ADRIYALA SHAFT PROJECT - [N06000016]SCCL, TELANGANA	12/2009	212.34 1,228.39	1,228.39	1,228.77	03/2013 09/2012	09/2015	30	478.5
16	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL, CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,583.65	03/2014 -	03/2016	24	0
17	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL, CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,560.52	03/2014 -	03/2016	24	0
18	MAGADH OC 20 MTY (CCL) - [N06000015]CCL, JHARKHAND	08/2008	469.78 -	706.40	44.65	07/2012 -	03/2016	44	50.37
19	CHURCHA ROUG (1.35 MTY) - [N06000046]SECL, CHHATISGARH	06/2008	462.35 -	462.35	273.00	03/2014 -	03/2016	24	0
20	RAJMAHAL OC EXP. - [N06000056]ECL, JHARKHAND	09/2009	153.82 -	153.82	42.46	03/2014 -	03/2016	24	0
21	PENGANGA OC - [N06000066]WCL, MAHARASHTRA	10/2008	339.77 -	339.77	1.69	03/2014 -	03/2016	24	0
22	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24	0
23	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL, TELANGANA	12/2009	418.97 -	418.97	229.11	03/2012 -	03/2016	48	0
24	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL, TELANGANA	03/2010	181.19 -	181.19	36.13	03/2012 -	03/2016	48	0
25	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH	12/2009	321.42 -	321.50	211.59	03/2014 -	03/2016	24	.02
26	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL, JHARKHAND	08/2007	163.51 -	163.51	35.52	03/2011 -	03/2016	60	0
27	TAPIN OCP (2.5 MTY) - [N06000086]CCL, JHARKHAND	08/2008	264.68 -	264.68	142.19	03/2012 -	03/2016	48	0
28	RG OC -III EXTENSION (PHASE-II) PROJECT - [N06000100]SCCL, TELANGANA	06/2012	365.01 -	365.01	6.56	06/2015 -	06/2016	12	0
29	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL, ODISHA	01/2005	302.96 -	302.96	129.48	03/2010 -	03/2017	84	0
30	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL, JHARKHAND	12/2007	471.66 341.63	341.63	102.07	03/2011 -	03/2017	72	-27.57
31	JHANJRA R-VI SEAM PSLW - [N06000020]ECL, WEST BENGAL	11/2006	287.18 -	287.17	44.71	03/2011 -	03/2017	72	0
32	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL, ODISHA	12/2007	457.77 -	457.77	120.75	03/2013 -	03/2017	48	0
33	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]MCL, ODISHA	12/2007	172.08 -	172.08	146.04	03/2010 -	03/2017	84	0
34	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL, ODISHA	08/2008	207.28 -	207.28	170.25	03/2012 -	03/2017	60	0
35	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.63 -	479.63	118.51	03/2013 -	03/2017	48	0
36	JAGANNATHPOR OC - [N06000075]SECL, CHHATISGARH	09/2008	152.43 -	152.43	21.55	03/2015 -	03/2017	24	0
37	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL, JHARKHAND	12/2007	179.87 -	179.87	60.93	03/2012 -	03/2017	60	0
38	KARMA OCP (1.0 MTY) - [N06000088]CCL, JHARKHAND	06/2009	162.46 -	162.46	55.96	03/2014 -	03/2017	36	0

(September 2014) All Cost/
Expenditure in
Rs. crore

						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
39	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL, TELANGANA	07/2012	417.33 -	417.33	2.22	07/2016 -	03/2017	8	0
40	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29 -	242.29	0.30	03/2015 -	03/2018	36	0
41	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL, TELANGANA	07/2011	447.06 -	447.06	29.03	03/2015 -	03/2018	36	0
42	NEYVELI NEW THERMAL POWER PROJECT (2X500 MW) - [N06000095]NLC, TAMIL NADU	06/2011	5,907.11 -	5,907.11	371.49	12/2015 -	04/2018	28	0
43	MOONIDIH XV SEAM UG - [N06000098]BCCL, JHARKHAND	08/2011	1,230.27 2,500.00	1,230.27	1,000.00	04/2015 12/2018	04/2019	48	0
44	TALABIRA OCP - [N06000043]MCL, ODISHA	03/2008	447.72 -	447.72	52.34	03/2016 -	03/2020	48	0
45	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL, ODISHA	02/2008	395.87 -	395.87	76.74	03/2015 -	03/2021	72	0
46	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL, CHHATISGARH	06/2008	1,188.31 -	7,612.33	755.52	03/2013 -	03/2023	120	540.6
	Total		29,523.97 -	40,059.98	17,670.72				
	STEEL								
47	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL, ANDHRA PRADESH	06/2006	108.00 216.68	216.68	164.85	09/2008 12/2013	10/2014	73	100.63
48	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL, ANDHRA PRADESH	10/2005	8,692.00 12,291.00	12,291.00	10,976.01	10/2009 10/2012	12/2014	62	41.41
49	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL, WEST BENGAL	06/2008	14,443.00 -	16,408.00	16,340.70	12/2011 -	12/2014	36	13.61
50	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL, JHARKHAND	05/2010	6,325.00 -	6,325.00	4,856.37	12/2011 -	12/2014	36	0
51	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHHATISGARH - [N12000078]SAIL, CHHATISGARH	07/2012	332.65 -	332.65	137.76	08/2014 -	01/2015	5	0
52	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL, ODISHA	10/2012	160.48 -	160.48	97.05	09/2014 -	01/2015	4	0
53	BAILADILA IRON ORE PROJECT DEPOSIT-11B (NMDC) - [N12000018]NMDC, CHHATISGARH	01/2007	295.89 607.17	607.17	376.30	12/2011 01/2015	03/2015	39	105.2
54	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]RINL, MULTI STATE	07/2007	480.00 -	450.00	322.07	09/2009 05/2012	03/2015	66	-6.25
55	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]SAIL, ODISHA	08/2010	11,812.00 -	11,812.00	11,497.14	03/2013 -	03/2015	24	0
56	1.2 MTPA PELLET PLANT PROJECT, DONIMALAI (NMDC) - [N12000072]NMDC, KARNATAKA	04/2011	572.00 -	572.00	404.31	04/2013 09/2014	03/2015	23	0

(September 2014) All Cost/
Expenditure in
Rs. crore

						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
57	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,KARNATAKA	02/2011	898.55 -	898.55	343.43	05/2013 01/2015	03/2015	22	0
58	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL, WEST BENGAL	08/2010	2,875.00 -	2,875.00	2,355.92	12/2012 -	03/2015	27	0
59	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079]SAIL,ODISHA	06/2012	237.09 -	237.09	87.87	12/2014 -	03/2015	3	0
60	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL,ODISHA	11/2011	254.55 -	254.55	114.35	11/2013 -	06/2015	19	0
61	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA	12/2011	187.33 -	187.33	138.60	10/2013 -	08/2015	22	0
62	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	13,392.35	03/2013 -	09/2015	30	0
	Total		64,938.54 -	70,892.50	61,605.08				
	<u>PETROLEUM</u>								
63	MRPL PHASE-III EXPANSION - [N16000114]MANGALORE REFIN,KARNATAKA	08/2008	12,412.00 -	12,160.26	-	01/2012 -	09/2014	32	-2.03
64	WAX PROJECT - [N16000101]NRL,ASSAM	06/2010	576.60 676.05	676.05	560.73	12/2013 05/2014	10/2014	10	17.25
65	POLYPROPYLENE UNIT - [N16000113]MANGALORE REFIN,KARNATAKA	05/2009	1,803.78 -	1,803.78	1,016.69	07/2012 -	10/2014	27	0
66	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]BPCL,MAHARASHTRA	08/2009	246.81 276.83	276.83	261.43	08/2012 -	10/2014	26	12.16
67	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,ANDHRA PRADESH	03/2009	3,597.00 2,730.00	2,730.00	3,128.58	09/2011 03/2012	11/2014	38	-24.1
68	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]ONGC,MULTI STATE	03/2010	3,241.03 6,638.94	6,638.94	2,192.69	03/2013 11/2014	11/2014	20	104.84
69	102 MW WIND POWER PROJECT - [N16000119]ONGC,RAJASTHAN	07/2010	1,106.00 -	678.02	405.00	06/2012 -	12/2014	30	-38.7
70	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,ANDHRA PRADESH	01/2006	672.00 1,038.00	1,038.00	991.73	10/2011 -	12/2014	38	54.46
71	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL,ODISHA	07/2009	199.75 -	199.75	145.55	07/2013 -	12/2014	17	0
72	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]ONGC,MULTI STATE	10/2013	429.06 -	429.06	-	10/2014 -	12/2014	2	0
73	GAS TURBINE GENERATION SET - [N18000146]OIL,ASSAM	07/2009	216.88 -	216.88	186.44	10/2011 12/2014	12/2014	38	0

(September 2014) All Cost/
Expenditure in
Rs. crore

						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
74	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL, ASSAM	08/2008	144.02 204.29	204.29	155.04	06/2012 09/2013	12/2014	30	41.85
75	DABHOL BANGALORE PIPELINE PROJECT PHASE-II - [N16000147]GAIL, MULTI STATE	06/2009	486.00 -	486.00	107.14	09/2013 -	02/2015	17	0
76	PARADIP REFINERY PROJECT - [N16000058]IOCL, ODISHA	02/2009	29,777.00 34,555.00	34,555.00	26,919.64	11/2012 11/2013	03/2015	28	16.05
77	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]ONGC, TRIPURA	07/2008	288.04 288.04	253.66	216.68	08/2012 -	03/2015	31	-11.94
78	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL, MULTI STATE	08/2010	8,140.00 -	8,140.00	7,117.42	02/2014 -	03/2015	13	0
79	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC, GUJARAT	03/2009	302.26 -	240.95	106.67	09/2012 -	03/2015	30	-20.28
80	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC, MAHARASHTRA	03/2011	861.79 -	761.68	634.95	05/2013 06/2014	03/2015	22	-11.62
81	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL, MAHARASHTRA	03/2012	1,419.00 -	1,419.00	771.67	12/2014 -	03/2015	3	0
82	IOR OF B-173A FIELD - [N16000140]ONGC, MULTI STATE	01/2012	352.49 -	352.49	99.82	03/2014 -	04/2015	13	0
83	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC, MAHARASHTRA	06/2007	3,248.78 5,633.44	6,000.00	5,867.78	08/2010 03/2012	05/2015	57	84.68
84	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC, MULTI STATE	11/2010	331.20 -	269.10	190.04	08/2013 -	05/2015	21	-18.75
85	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC, MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	598.34	03/2015 -	05/2015	2	29.42
86	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC, MAHARASHTRA	03/2012	2,592.17 -	2,592.17	310.34	05/2014 -	05/2015	12	0
87	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC, MULTI STATE	04/2012	600.17 -	600.17	248.92	12/2014 -	05/2015	5	0
88	PIPELINE REPLACEMENT PROJECT-3 - [N16000137]ONGC, MULTI STATE	04/2012	2,547.26 -	1,417.00	1,304.57	05/2014 -	05/2015	12	-44.37
89	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC, MULTI STATE	04/2003	429.82 3,955.21	3,955.21	3,413.13	04/2006 04/2016	06/2015	110	820.2
90	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL, MULTI STATE	06/2009	2,915.00 -	2,300.00	1,408.97	12/2012 06/2015	06/2015	30	-21.1
91	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL, MULTI STATE	12/2009	463.32 -	330.47	270.86	06/2011 03/2012	07/2015	49	-28.67
92	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL, MULTI STATE	12/2009	309.81 462.79	462.79	94.94	10/2014 -	10/2015	12	49.38

(September 2014) All Cost/
Expenditure in
Rs. crore

						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
93	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	888.80	10/2011 -	10/2015	48	67.62
94	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,283.65	01/2012 -	10/2015	45	70.49
95	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 1,200.00	1,200.00	55.28	03/2015 11/2015	11/2015	8	37.72
96	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	736.65	469.52	09/2011 -	12/2015	51	0
97	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	1,019.33	09/2012 -	12/2015	39	0
98	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE	06/2010	2,523.00 -	2,523.00	1,013.04	01/2014 -	12/2015	23	0
99	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	913.00	326.01	07/2015 -	12/2015	5	0
100	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96 -	191.96	53.98	05/2015 -	12/2015	7	0
101	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 -	2,378.86	1,711.73	03/2013 03/2015	03/2016	36	-3.5
102	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	270.00	-	12/2014 03/2016	03/2016	15	0
103	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	723.64	-	03/2013 -	06/2016	39	0
104	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL,GUJARAT	12/2011	160.00 -	160.00	-	03/2014 -	07/2016	28	0
105	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	08/2006	94.00 352.56	352.56	10.60	09/2012 03/2017	03/2017	54	275.06
106	AHMEDABAD REDEVELOPMENT PROJECT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10 -	1,916.10	1,160.14	12/2014 -	12/2017	36	0
107	MEHESANA REDEVELOPMENT PROJECT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	3,823.00	1,076.57	04/2015 -	12/2017	32	0
108	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63 -	2,189.63	1,039.42	12/2014 -	12/2018	48	0
109	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18 -	7,596.18	13.50	01/2013 -	02/2019	73	0
110	SURAT PARADIP PIPELINE PROJECT - [N16000163]GAIL,MULTI STATE	10/2012	10,281.00 -	10,281.00	1.36	04/2015 -	12/2020	68	0
	Total		120,041.33 -	133,821.78	68,848.69				

(September 2014) All Cost/
Expenditure in
Rs. crore

						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
	<u>POWER</u>								
111	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]PGCIL,MULTI STATE	08/2008	2,360.95 -	2,580.90	-	08/2012 -	09/2014	25	9.32
112	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118]PGCIL,GUJARAT	01/2012	259.28 -	259.28	169.82	01/2014 -	10/2014	9	0
113	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 623.44	994.85	833.58	07/2013 08/2014	11/2014	16	136.3
114	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 -	2,074.86	1,657.94	03/2013 -	11/2014	20	0
115	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000107]PGCIL,CHHATISGARH	08/2011	1,391.97 -	1,391.97	-	12/2013 -	11/2014	11	0
116	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL,MADHYA PRADESH	03/2012	213.78 -	213.78	153.34	03/2014 -	11/2014	8	0
117	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 -	477.69	495.59	09/2010 -	12/2014	51	0
118	SYSTEM STRENGTHENING IN NR FOR SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,022.39	08/2012 -	12/2014	28	0
119	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	487.49	305.72	06/2014 -	12/2014	6	0
120	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	437.80	02/2014 -	12/2014	10	0
121	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19 -	2,743.19	2,368.80	12/2013 -	02/2015	14	0
122	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]PGCIL,MULTI STATE	03/2011	2,569.25 -	2,569.25	2,550.67	03/2014 -	02/2015	11	0
123	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]PGCIL,MULTI STATE	09/2011	1,366.34 -	1,366.34	1,123.46	12/2013 -	02/2015	14	0
124	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM	01/2011	368.72 -	913.63	656.12	07/2006 12/2015	02/2015	103	147.78
125	BARH STPP STAGE -II - [N18000047]NTPC,BIHAR	02/2008	7,341.04 -	7,341.04	7,902.00	08/2013 -	03/2015	19	0

(September 2014) All Cost/
Expenditure in
Rs. crore

						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
126	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. - [N18000076]PGCIL,MULTI STATE	03/2010	4,672.99 -	4,672.99	3,381.37	11/2012 -	03/2015	28	0
127	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 -	752.64	425.52	07/2013 -	03/2015	20	0
128	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATISGARH	05/2011	1,961.87 -	1,961.87	1,528.65	05/2014 -	03/2015	10	0
129	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,479.66	09/2014 -	03/2015	6	0
130	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	310.81	11/2013 -	03/2015	16	0
131	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH	11/2011	2,127.51 -	2,127.51	1,943.33	07/2014 -	03/2015	8	0
132	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	412.62	11/2014 -	03/2015	4	0
133	KOLDAM HEP (NTPC) - [180100211]NTPC,HIMACHAL PRADESH	10/2002	4,527.15 7,220.00	7,220.00	6,077.00	04/2009 -	05/2015	73	59.48
134	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 -	1,746.65	570.83	08/2014 -	05/2015	9	0
135	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	142.92	04/2015 -	05/2015	1	0
136	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	9,188.20	08/2013 -	06/2015	22	0
137	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	1,867.60	12/2012 -	06/2015	30	0
138	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	-	01/2013 -	06/2015	29	0
139	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,319.96	11/2013 -	06/2015	19	0

(September 2014) All Cost/
Expenditure in
Rs. crore

						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
140	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	1,216.96	08/2014 -	06/2015	10	0
141	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATTISGARH	01/2012	1,422.85 -	1,422.85	799.32	01/2015 -	06/2015	5	0
142	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAND AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	-	10/2014 -	06/2015	8	0
143	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99 1,128.38	1,128.38	909.40	08/2013 -	09/2015	25	96.59
144	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	3,972.68	10/2012 -	12/2015	38	0
145	TRANSM SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B - [N18000077]PGCIL, WEST BENGAL	04/2010	4,404.57 -	4,404.57	661.15	01/2015 -	12/2015	11	0
146	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	892.43	11/2012 -	12/2015	37	0
147	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATTISGARH	03/2012	9,569.76 -	9,569.76	-	06/2015 -	12/2015	6	0
148	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC, WEST BENGAL	09/2005	1,061.38 -	1,929.15	1,551.17	09/2009 -	03/2016	78	81.76
149	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	415.06	11/2011 -	03/2016	52	0
150	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	694.44	11/2012 -	03/2016	40	0
151	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,086.62	04/2013 -	03/2016	35	0
152	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	6,749.18 6,749.18	6,749.18	4,726.00	07/2011 -	08/2016	61	0
153	KISHANGANGA HEP - [N18000031]NHPC,JAMMU AND KASHMIR	07/2007	3,642.04 3,642.04	5,497.72	3,644.34	01/2016 -	11/2016	10	50.95
154	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 -	4,653.95	3,241.37	12/2009 03/2017	03/2017	87	86.39
155	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	12/2003	8,692.97 -	8,693.00	10,264.00	12/2009 -	03/2017	87	0
156	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	2,202.00	03/2013 -	03/2018	60	29.14

(September 2014) All Cost/
Expenditure in
Rs. crore

						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
157	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	12/2011	15,166.19 -	15,166.19	5,031.00	12/2016 -	03/2018	15	0
158	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	7,921.47	3,051.00	09/2016 -	03/2018	18	0
159	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 2,998.00	9,395.18	3,102.00	11/2016 -	03/2018	16	0
160	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	1,527.00	140.00	08/2017 -	03/2018	7	0
161	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	02/2013	11,638.55 -	11,638.55	1,471.00	09/2017 -	03/2018	6	0
162	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	909.81	07/2010 02/2016	05/2018	94	79.77
163	PARBATI HEP (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	5,366.00	4,667.37	09/2009 -	07/2018	106	36.9
164	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,UTTARAKHAND	08/2008	2,491.58 3,745.08	3,745.08	498.11	07/2014 -	07/2018	48	50.31
165	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	6,285.33	6,943.84	09/2010 -	12/2018	99	0
166	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	11/2012	11,846.00 -	11,846.00	1,846.00	05/2017 -	03/2019	22	0
	Total		186,803.25 -	201,159.31	112,262.77				
	<u>RAILWAYS</u>								
167	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	608.02	593.82	03/1994 -	10/2014	247	282.96
168	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	432.72	414.84	12/2009 03/2011	12/2014	60	300.67
169	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 -	2,363.00	1,473.59	03/2009 12/2012	12/2014	69	156.57
170	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	09/2001	120.00 245.39	245.39	232.11	12/2008 -	12/2014	72	104.49
171	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	171.02 -	171.02	155.41	06/2013 -	12/2014	18	0
172	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,MULTI STATE	03/1984	520.00 835.04	835.04	646.73	03/1995 -	03/2015	240	60.58
173	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	445.40	180.72	03/2007 03/2007	03/2015	96	13.2
174	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	272.39	141.55	03/2012 12/2013	03/2015	36	59.2

(September 2014) All Cost/
Expenditure in
Rs. crore

						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
175	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	334.90	230.66	06/2004 -	12/2015	138	72.57
176	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 -	2,921.00	2,252.44	10/2007 12/2012	12/2015	98	367.76
177	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	261.70 -	261.70	156.22	02/2006 -	12/2015	118	0
178	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	800.00	798.47	03/2010 -	12/2015	69	16.41
179	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	401.81 495.44	1,814.10	392.88	03/2004 12/2010	03/2016	144	351.48
180	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NEFR,MULTI STATE	04/2000	733.00 733.00	2,483.04	1,673.08	12/2008 -	03/2016	87	238.75
181	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	874.57	606.09	03/2013 -	03/2016	36	81.45
182	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,298.42	78.05	03/2014 -	03/2016	24	0
183	KATAKHAL TO BHAIRABI - [N22000126]NEFR,ASSAM	04/1998	227.90 -	331.40	174.44	12/2012 -	03/2016	39	45.41
184	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NEFR,ASSAM	04/1996	1,676.31 -	5,185.44	4,452.04	03/2009 -	03/2016	84	209.34
185	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 -	388.67	111.16	12/2015 -	03/2016	3	25.6
186	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NEFR,TRIPURA	04/1999	895.00 -	1,242.25	994.65	03/2007 -	03/2016	108	38.8
187	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	121.21	03/2016 -	06/2016	3	0
188	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	184.91	64.70	03/2015 -	12/2016	21	23.36
189	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 -	1,116.53	374.71	03/2010 03/2017	03/2017	84	243.55
190	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]NEFR,ASSAM	09/1997	1,500.00 -	4,996.19	3,326.02	04/2008 03/2014	06/2017	110	233.08
191	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,MANIPUR	04/2003	727.56 727.56	5,996.00	2,519.80	03/2011 03/2014	03/2018	84	724.12
192	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,TRIPURA	04/2008	813.34 -	1,741.00	752.27	03/2014 -	03/2018	48	114.06
193	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP,TELANGANA	04/2012	632.68 -	816.55	17.42	04/2012 03/2016	03/2018	71	29.06

(September 2014) All Cost/
Expenditure in
Rs. crore

						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
194	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	19,565.00	9,965.25	11/2002 -	12/2018	193	682.6
195	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 6,213.84	7,012.84	1,820.40	03/2014 03/2019	03/2019	60	32.32
196	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR, MIZORAM	04/2008	619.34 -	2,393.48	192.81	04/2014 03/2020	03/2020	71	286.46
197	SEVOK RANGPO, NEFR - [N22000102]NEFR, SIKKIM	04/2008	1,339.48 -	3,375.42	85.64	12/2015 -	03/2020	51	151.99
198	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NEFR, NAGALAND	04/2006	850.00 -	2,446.57	10.23	03/2015 03/2020	03/2020	60	187.83
	Total		28,509.69 -	76,350.68	35,009.41				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
199	LUCKNOW-RAIBAREILI - [N24000207]NHAI, UTTAR PRADESH	07/1999	635.90 -	635.90	608.30	07/2012 -	09/2014	26	0
200	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, ASSAM	12/2003	245.00 -	245.00	491.20	03/2008 01/2015	10/2014	79	0
201	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI, ASSAM	12/2003	200.00 -	200.00	288.80	06/2008 -	10/2014	76	0
202	KOTA BYPASS, RJ-4, NH-76 (NHAI) - [240106297]NHAI, RAJASTHAN	12/2003	275.00 -	250.39	285.30	10/2008 -	11/2014	73	-8.95
203	DEOLI-KOTA - [N24000148]NHAI, RAJASTHAN	01/2011	593.00 -	593.00	759.90	07/2013 -	11/2014	16	0
204	DEVELOPMENT OF ADEQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI, TAMIL NADU	06/2011	600.00 -	600.00	381.50	06/2013 -	11/2014	17	0
205	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI, ANDHRA PRADESH	04/2011	571.00 -	571.00	-	10/2013 -	11/2014	13	0
206	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI, UTTAR PRADESH	01/2013	373.47 -	373.47	268.60	07/2014 -	11/2014	4	0
207	REENGUS SIKAR - [N24000227]NHAI, RAJASTHAN	03/2012	333.51 -	333.51	270.80	09/2014 -	11/2014	2	0
208	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, ASSAM	12/2003	157.47 157.47	154.57	267.60	09/2007 03/2014	12/2014	87	-1.84
209	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, UTTAR PRADESH	12/2003	155.00 -	201.66	191.70	09/2008 -	12/2014	75	30.1
210	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, ASSAM	12/2003	280.00 -	280.00	366.10	02/2009 -	12/2014	70	0
211	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, ASSAM	12/2003	167.64 -	167.64	138.80	11/2008 -	12/2014	73	0

(September 2014) All Cost/
Expenditure in
Rs. crore

						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
212	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	200.00	207.20	04/2009 -	12/2014	68	0
213	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	332.94	525.80	09/2008 -	12/2014	75	0
214	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	251.03	384.70	10/2008 -	12/2014	74	0
215	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	175.96	286.70	04/2008 01/2015	12/2014	80	0
216	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	264.72	315.70	06/2008 -	12/2014	78	0
217	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	198.16	341.00	04/2008 01/2015	12/2014	80	0
218	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	208.00	334.10	04/2008 04/2015	12/2014	80	0
219	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	211.70	05/2008 04/2015	12/2014	79	0
220	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 331.23	363.74	240.40	07/2009 -	12/2014	65	85.58
221	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	557.00	1,123.00	02/2010 -	12/2014	58	0
222	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	666.40	05/2010 -	12/2014	55	0
223	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	1,509.10	2,613.00	09/2012 -	12/2014	27	0
224	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	795.00	1,132.00	05/2012 -	12/2014	31	0
225	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	353.37	446.20	10/2011 -	12/2014	38	0
226	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	1,693.75	2,762.00	08/2011 -	12/2014	40	0
227	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	12/2014	20	0
228	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	899.70	03/2013 -	12/2014	21	0
229	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	996.80	05/2013 -	12/2014	19	0
230	AMRITSAR-PATHANKOT - [N24000147]NHAI,PUNJAB	05/2010	705.00 -	705.00	2,208.00	11/2012 -	12/2014	25	0
231	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	193.45	66.01	11/2012 -	12/2014	25	0
232	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,292.00	03/2013 -	12/2014	21	0

(September 2014) All Cost/
Expenditure in
Rs. crore

						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
233	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	1,173.00	07/2013 -	12/2014	17	0
234	PATNA-MUZZAFFARPUR - [N24000165]NHAI, BIHAR	08/2010	671.30 -	671.30	632.70	02/2013 -	12/2014	22	0
235	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, UTTAR PRADESH	02/2011	1,141.00 -	1,141.00	2,157.00	08/2013 -	12/2014	16	0
236	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI, TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,321.00	12/2013 -	12/2014	12	0
237	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI, TAMIL NADU	05/2010	374.00 -	374.00	148.80	05/2013 -	12/2014	19	0
238	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI, GUJARAT	09/2010	805.39 -	805.39	841.90	03/2013 -	12/2014	21	0
239	JORBAT - BARAPANI - [N24000180]NHAI, MEGHALAYA	01/2011	536.00 -	536.00	746.90	01/2014 -	12/2014	11	0
240	PATNA-BAKTARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, BIHAR	09/2011	574.00 -	574.00	982.40	03/2014 -	12/2014	9	0
241	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI, BIHAR	05/2011	511.54 -	511.54	1,179.00	11/2013 -	12/2014	13	0
242	SRINAGAR TO BANIHAL - [N24000189]NHAI, JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	323.00	06/2014 -	12/2014	6	0
243	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI, ODISHA	11/2011	909.00 -	909.00	974.30	05/2014 -	12/2014	7	0
244	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, MULTI STATE	02/2011	998.79 -	998.79	1,597.00	08/2013 -	12/2014	16	0
245	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI, MULTI STATE	12/2011	1,047.00 -	1,047.00	294.60	06/2014 -	12/2014	6	0
246	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI, MAHARASHTRA	04/2012	484.19 -	484.19	285.50	10/2014 -	12/2014	2	0
247	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI, TAMIL NADU	09/2011	485.00 -	485.00	362.20	08/2013 -	02/2015	18	0
248	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, ASSAM	12/2003	199.81 -	385.13	159.20	04/2009 -	03/2015	71	92.75
249	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI, ASSAM	12/2003	195.00 -	195.00	280.20	06/2008 -	03/2015	81	0
250	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI, ASSAM	12/2003	237.80 -	237.80	321.40	06/2008 -	03/2015	81	0
251	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, ASSAM	12/2003	225.00 -	225.00	276.40	06/2008 04/2015	03/2015	81	0
252	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061]NHAI, ASSAM	12/2003	212.00 333.83	386.10	126.70	09/2007 -	03/2015	90	82.12
253	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI, MULTI STATE	12/2003	232.45 -	232.45	317.20	09/2010 -	03/2015	54	0

(September 2014) All Cost/
Expenditure in
Rs. crore

						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
254	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	03/2015	40	106.5
255	MURADABAD-BAREILLY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,415.00	06/2013 -	03/2015	21	0
256	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	535.00	52.18	12/2013 -	03/2015	15	0
257	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	406.60	04/2014 -	03/2015	11	0
258	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	825.40	07/2013 -	03/2015	20	0
259	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	835.00	475.90	01/2014 -	03/2015	14	0
260	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	500.29	632.80	08/2013 -	03/2015	19	0
261	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	356.40	250.60	07/2014 -	03/2015	8	0
262	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT	03/2012	828.00 -	828.00	763.50	09/2014 -	03/2015	6	0
263	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	2,188.00	05/2014 -	05/2015	12	0
264	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	624.00	441.40	04/2014 -	05/2015	13	0
265	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	230.00	251.50	06/2005 -	06/2015	120	0
266	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	280.13	173.80	11/2008 -	06/2015	79	80.68
267	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	465.50	308.10	09/2007 -	06/2015	93	33.7
268	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	572.30	886.90	10/2011 -	06/2015	44	0
269	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	927.40	07/2013 -	06/2015	23	0
270	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	1,078.84	1,906.00	08/2013 -	06/2015	22	0
271	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	2,786.00	08/2014 -	07/2015	11	0
272	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	398.00	461.90	02/2014 -	09/2015	19	0
273	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	787.90	09/2014 -	10/2015	13	0

(September 2014) All Cost/
Expenditure in
Rs. crore

						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
274	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	2,388.00	2,249.00	06/2014 -	11/2015	17	0
275	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	682.00	729.40	10/2013 -	11/2015	25	0
276	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	495.40	12/2009 -	12/2015	72	0
277	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	325.00	609.50	05/2013 -	12/2015	31	0
278	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,134.00	03/2014 -	12/2015	21	0
279	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	209.00	38.77	01/2013 -	12/2015	35	0
280	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	398.50	09/2013 -	12/2015	27	0
281	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	591.50	03/2013 -	12/2015	33	0
282	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	580.43	430.20	08/2013 -	12/2015	28	0
283	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	141.10	01/2014 -	12/2015	23	0
284	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	719.20	07/2014 -	12/2015	17	0
285	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	478.00	321.20	10/2013 -	12/2015	26	0
286	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	942.69	286.60	06/2014 -	12/2015	18	0
287	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	309.56	258.40	04/2010 01/2016	01/2016	69	42.25
288	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	867.00	598.60	02/2015 -	02/2016	12	0
289	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	156.60	08/2012 -	03/2016	43	0
290	NASHRI CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	06/2010	2,159.00 -	2,159.00	622.70	06/2015 -	05/2016	11	0
291	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,170.00	07/2015 -	06/2016	11	0
292	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	281.31	181.10	02/2010 -	07/2016	77	2.29
293	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	39.55	09/2013 -	12/2016	39	0
294	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2016	35	0

(September 2014) All Cost/
Expenditure in
Rs. crore

						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
	Total		67,308.76 -	69,375.76	67,825.91				
	<u>SHIPPING AND PORTS</u>								
295	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053]SHIPP.,MAHARASHTRA	10/2010	966.46 -	994.82	427.54	02/2014 01/2015	01/2015	11	2.93
296	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 1,460.00	2,098.56	1,020.94	12/2010 09/2012	03/2015	51	70.89
	Total		2,194.46 -	3,093.38	1,448.48				
	<u>TELECOMMUNICATIONS</u>								
297	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058]BSNL,UTTARAKHAND	01/2009	149.15 -	158.72	86.05	06/2009 -	12/2014	66	6.42
298	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL,ASSAM	06/2007	336.81 -	336.81	195.94	01/2009 -	12/2014	71	0
299	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	384.00	48.95	10/2010 11/2015	03/2015	53	0
	Total		869.96 -	879.53	330.94				
	<u>URBAN DEVELOPMENT</u>								
300	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA - [N28000078]CPWD,BIHAR	11/2006	2,727.89 -	2,727.89	2,637.11	03/2010 -	10/2014	55	0
301	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	205.00	93.74	03/2012 -	01/2015	34	0
302	FARIDABAD EXTENSION - [N28000057]DMRC,DELHI	09/2011	2,494.00 -	2,494.00	685.21	09/2014 -	05/2015	8	0
303	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD,WEST BENGAL	01/2009	225.81 -	225.81	17.60	06/2012 -	05/2015	35	0
304	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD,ODISHA	11/2012	238.43 -	238.43	-	02/2015 -	08/2015	6	0
305	C/O NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 -	315.00	53.96	06/2015 -	08/2015	2	0

(September 2014) All Cost/
Expenditure in
Rs. crore

						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
306	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	15.60	11/2014 -	10/2015	11	0
307	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85 -	261.85	101.52	05/2013 -	10/2015	29	0
308	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	884.30	103.45	08/2014 -	01/2016	17	0
309	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI	05/2012	405.01 -	405.01	-	12/2014 -	04/2016	16	0
310	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	-	03/2016 -	05/2016	2	0
311	CONSTRUCTION OF CENTRAL ACADEMY FOR PUBLIC TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	188.87	10.64	12/2014 -	12/2016	24	0
312	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	-	09/2015 -	12/2016	15	0
	Total		8,545.42 -	8,545.42	3,718.83				
	Grand Total		550,384.33	652,164.21	400,612.58				

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(September 2014)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	03/2015	62.57	54
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	12/2008 -	11/2014	31.12	71
	Total		16,663.00 -	22,947.00				
	<u>CIVIL AVIATION</u>							
3	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]	05/2010	335.61 -	388.53	05/2012 -	10/2014	15.77	29
	Total		335.61 -	23,335.53				
	<u>COAL</u>							
4	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	09/2015	478.50	30
5	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]	12/2009	321.42 -	321.50	03/2014 -	03/2016	0.02	24
6	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37	44
7	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	06/2008	1,188.31 -	7,612.33	03/2013 -	03/2023	540.60	120
8	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,321.86	06/2009 -	10/2014	63.58	64
9	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,602.74	03/2012 -	11/2014	34.63	32
	Total		9,127.17 -	43,128.75				
	<u>PETROLEUM</u>							
10	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	08/2006	94.00 -	352.56	09/2012 -	03/2017	275.06	54
11	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]	08/2008	144.02 -	204.29	06/2012 -	12/2014	41.85	30
12	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]	08/2009	246.81 -	276.83	08/2012 -	10/2014	12.16	26
13	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79	10/2014 -	10/2015	49.38	12
14	DEV OF G1 AND GS-15 (ONGCL) - [160100231]	04/2003	429.82 -	3,955.21	04/2006 -	06/2015	820.20	110

(September 2014)

Date of Commissioning (Month/Year)								
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
15	WAX PROJECT - [N16000101]	06/2010	576.60 -	676.05	12/2013 -	10/2014	17.25	10
16	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]	01/2006	672.00 -	1,038.00	10/2011 -	12/2014	54.46	38
17	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]	01/2006	732.00 -	1,227.00	10/2011 -	10/2015	67.62	48
18	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	11/2015	37.72	8
19	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	10/2015	70.49	45
20	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	05/2015	29.42	2
21	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]	03/2010	3,241.03 -	6,638.94	03/2013 -	11/2014	104.84	20
22	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]	06/2007	3,248.78 -	6,000.00	08/2010 03/2012	05/2015	84.68	57
23	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00 -	34,555.00	11/2012 -	03/2015	16.05	28
	Total		43,395.85 -	104,074.07				
	<u>POWER</u>							
24	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	994.85	07/2013 -	11/2014	136.30	16
25	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,128.38	08/2013 -	09/2015	96.59	25
26	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]	09/2005	1,061.38 -	1,929.15	09/2009 -	03/2016	81.76	78
27	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	07/2010 -	05/2018	79.77	94
28	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]	08/2008	2,360.95 -	2,580.90	08/2012 -	09/2014	9.32	25
29	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,745.08	07/2014 -	07/2018	50.31	48
30	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	4,653.95	12/2009 06/2016	03/2017	86.39	87
31	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	03/2018	29.14	60
32	KISHANGANGA HEP - [N18000031]	07/2007	3,642.04 -	5,497.72	01/2016 -	11/2016	50.95	10
33	PARBATI HEP (NHPC) II - [180100210]	09/2002	3,919.59 -	5,366.00	09/2009 -	07/2018	36.90	106
34	KOLDAM HEP (NTPC) - [180100211]	10/2002	4,527.15 -	7,220.00	04/2009 -	05/2015	59.48	73

(September 2014)

Date of Commissioning (Month/Year)								
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
35	BARH STPP(3X660MW) NTPC - [180100242	12/2003	8,692.97 -	8,693.00	12/2009 -	03/2017	0.00	87
	Total		34,823.04 -	152,708.26				
	<u>RAILWAYS</u>							
36	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	12/2009 -	12/2014	300.67	60
37	ETAWAH-MAINPURI (NL),NCR - [220100318	09/2001	120.00 -	245.39	12/2008 -	12/2014	104.49	72
38	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION [N22000162	04/2010	149.90 -	184.91	03/2015 -	12/2016	23.36	21
39	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007	04/1986	158.77 274.56	608.02	03/1994 -	10/2014	282.96	247
40	ELECTRIFICATION OF KHURJA-MEERUT- SAHARANPUR AND G'BAD-MEERUT - [N22000094	02/2008	171.10 -	272.39	03/2012 -	03/2015	59.20	36
41	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	334.90	06/2004 -	12/2015	72.57	138
42	KATAKHAL TO BHAIIRABI - [N22000126	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41	39
43	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164	04/2010	309.44 -	388.67	12/2015 -	03/2016	25.60	3
44	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	04/2006	325.00 -	1,116.53	03/2010 -	03/2017	243.55	84
45	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	445.40	03/2007 03/2007	03/2015	13.20	96
46	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	401.81 -	1,814.10	03/2004 -	03/2016	351.48	144
47	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107	04/2007	482.00 -	874.57	03/2013 -	03/2016	81.45	36
48	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009	03/1984	520.00 422.79	835.04	03/1995 -	03/2015	60.58	240
49	BHAIIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	619.34 -	2,393.48	04/2014 -	03/2020	286.46	71
50	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76	98
51	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD [N22000213	04/2012	632.68 -	816.55	04/2012 -	03/2018	29.06	71
52	BHOPAL BINA 3D LINE DOUBLING - [N22000077	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41	69
53	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	5,996.00	03/2011 -	03/2018	724.12	84
54	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	2,483.04	12/2008 -	03/2016	238.75	87

(September 2014)

Date of Commissioning (Month/Year)								
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
55	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	1,741.00	03/2014 -	03/2018	114.06	48
56	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	850.00 -	2,446.57	03/2015 -	03/2020	187.83	60
57	CONSTRUCTION OF NL FROM KUMARGHAT- AGARTALA [N22000194]	04/1999	895.00 -	1,242.25	03/2007 -	03/2016	38.80	108
58	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]	04/2002	921.00 -	2,363.00	03/2009 -	12/2014	156.57	69
59	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	3,375.42	12/2015 -	03/2020	151.99	51
60	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	06/2017	233.08	110
61	LUMDING-SILCHAR JIRIBAM, BADARPUR- BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	5,185.44	03/2009 -	03/2016	209.34	84
62	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60	193
63	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,012.84	03/2014 -	03/2019	32.32	60
	Total		23,380.83 -	223,930.08				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
64	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH- 25, KM.75-80.06 [240106221]	12/2003	155.00 -	201.66	09/2008 -	12/2014	30.10	75
65	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	06/2015	80.68	79
66	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	363.74	07/2009 -	12/2014	85.58	65
67	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	03/2015	92.75	71
68	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061]	12/2003	212.00 -	386.10	09/2007 -	03/2015	82.12	90
69	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	04/2010 -	01/2016	42.25	69
70	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	07/2016	2.29	77
71	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]	12/2003	348.16 -	465.50	09/2007 -	06/2015	33.70	93
72	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	03/2015	106.50	40
	Total		2,866.62 -	228,891.21				
	<u>SHIPPING AND PORTS</u>							

(September 2014)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
73	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053	10/2010	966.46 -	994.82	02/2014 -	01/2015	2.93	11
74	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016	11/2007	1,228.00 -	2,098.56	12/2010 -	03/2015	70.89	51
	Total		2,194.46 -	231,984.59				
	<u>STEEL</u>							
75	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038	06/2006	108.00 -	216.68	09/2008 -	10/2014	100.63	73
76	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018	01/2007	295.89 -	607.17	12/2011 06/2010	03/2015	105.20	39
77	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067	10/2005	8,692.00 -	12,291.00	10/2009 -	12/2014	41.41	62
78	EXPANSION OF IISCO STEEL PLANT - [N12000051	06/2008	14,443.00 -	16,408.00	12/2011 -	12/2014	13.61	36
	Total		23,538.89 -	261,507.44				
	<u>TELECOMMUNICATIONS</u>							
79	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058	01/2009	149.15 -	158.72	06/2009 -	12/2014	6.42	66
	Total		149.15 -	261,666.16				
	Grand Total		156,474.62	1,554,173.09				

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2014)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	12/2008 -	11/2014	31.12
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	03/2015	62.57
	Total		16,663.00 -	22,947.00			
	<u>CIVIL AVIATION</u>						
3	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]	05/2010	335.61 -	388.53	05/2012 -	10/2014	15.77
	Total		335.61 -	23,335.53			
	<u>COAL</u>						
4	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,321.86	06/2009 -	10/2014	63.58
5	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	06/2008	1,188.31 -	7,612.33	03/2013 -	03/2023	540.60
6	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37
7	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	09/2015	478.50
8	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.00 -	490.10	03/2017 -	03/2017	0.02
9	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,602.74	03/2012 -	11/2014	34.63
10	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]	12/2009	321.42 -	321.50	03/2014 -	03/2016	0.02
11	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	03/2016 -	03/2016	31.87
	Total		9,767.76 -	43,817.44			
	<u>PETROCHEMICALS</u>						
12	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	8,920.00	04/2012 -	-	63.35
	Total		5,460.61 -	52,737.44			
	<u>PETROLEUM</u>						

(September 2014)

Date of Commissioning (Month/Year)							
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
13	DEV OF G1 AND GS-15 (ONGCL) - [N160100231]	04/2003	429.82 -	3,955.21	04/2006 -	06/2015	820.20
14	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]	06/2007	3,248.78 -	6,000.00	08/2010 03/2012	05/2015	84.68
15	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00 -	34,555.00	11/2012 -	03/2015	16.05
16	WAX PROJECT - [N16000101]	06/2010	576.60 -	676.05	12/2013 -	10/2014	17.25
17	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]	03/2010	3,241.03 -	6,638.94	03/2013 -	11/2014	104.84
18	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	05/2015	29.42
19	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]	08/2009	246.81 -	276.83	08/2012 -	10/2014	12.16
20	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	03/2012	14,225.00 -	16,504.00	05/2016 -	05/2016	16.02
21	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	02/2012	666.00 -	701.00	11/2015 -	11/2015	5.26
22	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79	10/2014 -	10/2015	49.38
23	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]	01/2006	672.00 -	1,038.00	10/2011 -	12/2014	54.46
24	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]	01/2006	732.00 -	1,227.00	10/2011 -	10/2015	67.62
25	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	08/2006	94.00 -	352.56	09/2012 -	03/2017	275.06
26	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	10/2015	70.49
27	KOTA JOBNER PIPELINE PROJECT - [N16000170]	04/2011	276.26 -	276.27	12/2015 -	03/2015	0.00
28	RESITEMENT OF BILASPUR AND BISRAPUR DEPOTS TO KORBA (CHATTISGARH) - [N16000186]	01/2011	141.86 -	219.08	09/2016 -	12/2015	54.43
29	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	11/2015	37.72
30	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]	08/2008	144.02 -	204.29	06/2012 -	12/2014	41.85
	Total		58,704.97 -	131,383.11			
	<u>POWER</u>						
31	PARBATI HEP (NHPC) II - [180100210]	09/2002	3,919.59 -	5,366.00	09/2009 -	07/2018	36.90
32	KOLDAM HEP (NTPC) - [180100211]	10/2002	4,527.15 -	7,220.00	04/2009 -	05/2015	59.48
33	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	4,653.95	12/2009 06/2016	03/2017	86.39

(September 2014)

Date of Commissioning (Month/Year)							
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
34	BARH STPP(3X660MW) NTPC - [180100242	12/2003	8,692.97 -	8,693.00	12/2009 -	03/2017	0.00
35	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243	09/2005	1,061.38 -	1,929.15	09/2009 -	03/2016	81.76
36	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258	05/2005	1,779.29 -	2,159.07	09/2008 -	03/2013	21.34
37	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	07/2006	1,657.00 -	2,978.86	07/2010 -	05/2018	79.77
38	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014	11/2006	2,978.48 -	3,846.30	03/2013 -	03/2018	29.14
39	KISHANGANGA HEP - [N18000031	07/2007	3,642.04 -	5,497.72	01/2016 -	11/2016	50.95
40	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042	08/2008	2,491.58 -	3,745.08	07/2014 -	07/2018	50.31
41	PARE HYDRO ELECTRIC PROJECT - [N18000045	12/2008	573.99 -	1,128.38	08/2013 -	09/2015	96.59
42	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC [N18000065	08/2008	2,360.95 -	2,580.90	08/2012 -	09/2014	9.32
43	TRIPURA GAS BASED POWER PROJECT - [N18000071	07/2009	421.01 -	994.85	07/2013 -	11/2014	136.30
44	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119	01/2011	368.72 -	913.63	07/2006 02/2015	02/2015	147.78
	Total		36,971.05 -	183,090.00			
	<u>RAILWAYS</u>						
45	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007	04/1986	158.77 274.56	608.02	03/1994 -	10/2014	282.96
46	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009	03/1984	520.00 422.79	835.04	03/1995 -	03/2015	60.58
47	VIRAMGAM-BHILDI(WR),GC - [220100062	04/1990	155.66 -	548.01	- 03/2010	-	252.06
48	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	925.30	- -	02/2014	643.63
49	AMRAVATI-NARKHER NL(CR) - [220100118	06/1994	663.01 175.30	725.00	06/1999 -	-	9.35
50	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60
51	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135	04/1983	36.80 274.41	703.18	- -	-	1,810.82
52	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	968.60	12/2012 -	-	218.62
53	CALICUT-MANGALORE (DL) (SR) - [220100151	02/1996	240.00 -	579.37	- -	02/2012	141.40
54	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	401.81 -	1,814.10	03/2004 -	03/2016	351.48
55	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181	02/1997	514.68 -	2,820.00	- -	-	447.91

(September 2014)

Date of Commissioning (Month/Year)							
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
56	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR [220100183]	02/1997	295.00 -	1,289.92	- -	-	337.26
57	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30 -	1,038.00	03/1998 -	-	168.70
58	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	37.68 -	1,036.78	07/2012 -	-	2,651.54
59	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 -	800.00	- -	-	414.30
60	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	155.74 164.36	883.00	02/2009 -	03/2012	466.97
61	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	227.00 -	2,135.00	- -	-	840.53
62	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]	03/1997	677.97 1,062.36	1,651.54	- -	03/2015	143.60
63	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	06/2017	233.08
64	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	218.24 236.41	645.00	- -	12/2014	195.55
65	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	445.40	03/2007 03/2007	03/2015	13.20
66	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	194.07 -	334.90	06/2004 -	12/2015	72.57
67	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
68	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	1,630.97	05/2008 -	-	558.55
69	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	04/1997	501.69 335.77	1,043.56	03/2012 -	-	108.01
70	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	12/2009 -	12/2014	300.67
71	KATI HAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	492.98 -	1,022.64	12/2010 -	-	107.44
72	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00 -	1,566.00	- -	-	184.73
73	GULBARGA-BIDAR,SCR(NL) - [220100254]	02/1998	242.42 369.70	844.00	- 05/2009	03/2015	248.16
74	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) [220100255]	03/2002	863.23 -	1,072.51	- -	03/2015	24.24
75	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	625.30 408.76	847.75	06/2007 -	-	35.57
76	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	100.00 -	900.00	- -	-	800.00
77	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) [220100263]	03/1998	280.00 -	1,122.00	- -	-	300.71
78	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 -	1,045.20	- -	-	216.73

(September 2014)

Date of Commissioning (Month/Year)							
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
79	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	2,483.04	12/2008 -	03/2016	238.75
80	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69 -	3,176.10	12/2006 -	-	202.58
81	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	02/2011 -	-	191.48
82	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	02/1999	138.00 -	1,382.78	- -	-	902.01
83	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	1,423.98	03/2005 12/2008	-	1,172.55
84	JIND-SONEPAT (NL),NR - [220100280	01/2004	238.56 -	740.00	03/2012 -	12/2012	210.19
85	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	470.21 -	1,995.25	- -	-	324.33
86	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06
87	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	288.00	02/2009 02/2009	08/2014	73.33
88	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	5,996.00	03/2011 -	03/2018	724.12
89	KOSI BRIDGE (NL), ECR - [220100304	04/2002	322.95 -	341.41	03/2012 -	-	5.72
90	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	03/2009 -	12/2014	156.57
91	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76
92	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314	04/2001	470.92 727.13	1,225.90	- -	-	160.32
93	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315	01/2004	915.70 -	3,019.17	- -	03/2015	229.71
94	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316	04/2003	218.19 -	347.50	- -	-	59.26
95	ETAWAH-MAINPURI (NL),NCR - [220100318	09/2001	120.00 -	245.39	12/2008 -	12/2014	104.49
96	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	585.93	- -	12/2013	52.67
97	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	818.29	02/2015 -	02/2015	346.59
98	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	276.00	03/2009 03/2009	08/2014	106.88
99	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329	04/2003	136.62 -	289.93	12/2007 03/2010	-	112.22
100	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	332.92 283.95	477.88	03/2012 -	-	43.54
101	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032	04/2006	378.56 -	791.59	- -	-	109.11
102	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049	07/2006	743.00 -	1,117.11	03/2008 06/2008	-	50.35

(September 2014)

Date of Commissioning (Month/Year)							
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
103	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N22000052]	04/2003	98.74 -	337.30	- -	03/2012	241.60
104	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]	03/2005	470.09 -	1,417.97	- -	03/2012	201.64
105	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	385.54	03/2010 -	-	18.66
106	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41
107	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' -AGASTIYAMPALLI - [N22000079]	09/2007	404.19 -	1,383.45	- -	-	242.28
108	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	914.98	- -	03/2015	166.63
109	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	485.00	03/2011 -	-	185.29
110	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 -	420.00	- -	-	236.00
111	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	820.00	- -	-	79.82
112	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	430.33	- -	03/2017	115.17
113	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	300.00 -	532.87	- -	-	77.62
114	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,116.53	03/2010 -	03/2017	243.55
115	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,012.84	03/2014 -	03/2019	32.32
116	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	272.39	03/2012 -	03/2015	59.20
117	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,074.45	06/2005 -	-	265.50
118	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	1,741.00	03/2014 -	03/2018	114.06
119	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,393.48	04/2014 -	03/2020	286.46
120	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	359.86	- -	-	27.20
121	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	3,375.42	12/2015 -	03/2020	151.99
122	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]	04/2007	482.00 -	874.57	03/2013 -	03/2016	81.45
123	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2016	7.78
124	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	653.46	03/2014 -	-	0.04
125	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]	04/2009	259.51 -	533.38	12/2011 -	-	105.53

(September 2014)

(September 2014)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
126	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012 -	-	135.68
127	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	-	1.06
128	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	850.00 -	2,446.57	03/2015 -	03/2020	187.83
129	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]	04/2006	117.36 196.95	196.95	03/2011 -	-	67.82
130	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41
131	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	5,185.44	03/2009 -	03/2016	209.34
132	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	494.92	- -	-	67.77
133	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	913.48	- -	-	184.87
134	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	685.17	- -	-	53.63
135	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	02/2020	226.98
136	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITSURGARH-UDAIPUR - [N22000152]	04/2013	456.00 -	855.16	- -	-	87.54
137	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	-	17.92
138	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	218.39	- -	-	2.34
139	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	02/2019	226.23
140	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	651.17	- -	-	17.62
141	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	184.91	03/2015 -	12/2016	23.36
142	DANGOAPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	388.67	12/2015 -	03/2016	25.60
143	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	315.13	- -	12/2017	22.05
144	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
145	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
146	ATTIPPATTU-PUTTUR - [N22000184]	04/2008	446.87 -	528.00	- -	-	18.16
147	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,200.00	- -	-	129.22

(September 2014)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
148	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
149	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17
150	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]	04/1999	271.24 -	520.00	- -	-	91.71
151	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,280.83	- -	-	55.74
152	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
153	NEW BG LINE FROM DUDHNOI-MENDIPATAR - [N22000192]	04/1999	175.43 -	247.75	- -	-	41.22
154	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,242.25	03/2007 -	03/2016	38.80
155	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22	- -	-	109.04
156	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	-	173.71
157	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	247.00 -	951.24	- -	03/2015	285.12
158	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	222.95	- -	-	16.29
159	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	545.64	- -	-	229.06
160	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]	04/1999	523.17 -	1,418.21	- -	-	171.08
161	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	364.06	- -	-	47.95
162	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	04/2012 -	03/2018	29.06
163	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215]	04/2011	601.43 -	800.00	- -	-	33.02
164	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	499.30 -	2,501.05	- -	-	400.91
165	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70 -	279.70	- -	-	0.72
166	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	182.06 -	184.06	- -	-	1.10
167	PEN ROHA DOUBLING - [N22000254]	04/2007	98.74 -	203.00	- -	03/2015	105.59
168	PANVEL PEN DOUBLING - [N22000255]	04/2006	96.16 -	260.16	- -	-	170.55
169	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26
170	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	-	651.97

(September 2014)

Date of Commissioning (Month/Year)							
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
171	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97
172	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]	04/2008	184.26 -	2,000.00	- -	-	985.42
173	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	755.54	- -	-	163.25
174	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99	- -	-	183.41
175	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	-	24.09
176	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	-	57.65
177	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	- -	-	47.93
178	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,743.00	- -	-	79.63
179	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29
180	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	337.50	- -	-	0.00
181	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	329.97	- -	-	50.10
182	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	-	14.14
183	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00	- -	-	72.07
184	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	-	12.38
185	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]	04/1999	460.94 -	1,030.00	01/1999 -	-	123.46
186	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	468.48	01/1999 -	-	0.43
187	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	679.27 -	1,111.99	- -	-	63.70
188	JHARSUGUDA-RENGALI DOUBLING - [N22000317]	03/2006	201.00 -	201.17	- -	-	0.08
189	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10
190	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	174.69	12/2016 -	12/2016	17.42
	Total		70,767.31 -	365,136.41			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
191	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00 -	201.66	09/2008 -	12/2014	30.10
192	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	03/2015	92.75

(September 2014)

Date of Commissioning (Month/Year)							
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
193	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	11/2008 -	06/2015	80.68
194	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061	12/2003	212.00 -	386.10	09/2007 -	03/2015	82.12
195	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	363.74	07/2009 -	12/2014	85.58
196	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063	12/2003	217.61 -	309.56	04/2010 -	01/2016	42.25
197	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	02/2010 -	07/2016	2.29
198	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098	12/2003	348.16 -	465.50	09/2007 -	06/2015	33.70
199	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	03/2015	106.50
	Total		2,866.62 -	370,097.54			
	<u>SHIPPING AND PORTS</u>						
200	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL - [N25000003	10/2005	800.00 -	1,571.60	10/2008 -	-	96.45
201	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004	12/2005	154.84 -	253.36	- 01/2009	12/2010	63.63
202	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016	11/2007	1,228.00 -	2,098.56	12/2010 -	03/2015	70.89
203	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	06/2014	300.00
204	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA, KANDLA PORT TRUST - [N25000037	04/2005	882.00 -	1,060.00	02/2011 -	12/2012	20.18
205	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039	12/2005	702.00 -	755.50	03/2011 -	03/2013	7.62
206	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053	10/2010	966.46 -	994.82	02/2014 -	01/2015	2.93
207	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059	03/2007	245.67 -	373.22	04/2009 -	02/2011	51.92
	Total		5,128.97 -	377,804.60			
	<u>STEEL</u>						
208	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067	10/2005	8,692.00 -	12,291.00	10/2009 -	12/2014	41.41
209	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018	01/2007	295.89 -	607.17	12/2011 06/2010	03/2015	105.20
210	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038	06/2006	108.00 -	216.68	09/2008 -	10/2014	100.63

(September 2014)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
211	EXPANSION OF IISCO STEEL PLANT - [N12000051	06/2008	14,443.00 -	16,408.00	12/2011 -	12/2014	13.61
	Total		23,538.89 -	407,327.45			
	<u>TELECOMMUNICATIONS</u>						
212	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL [N26000058	01/2009	149.15 -	158.72	06/2009 -	12/2014	6.42
	Total		149.15 -	407,486.17			
	<u>URBAN DEVELOPMENT</u>						
213	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00 -	11,609.00	06/2011 -	03/2013	81.53
214	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI - [N28000048	11/2006	114.18 173.08	173.08	04/2009 -	-	51.59
	Total		6,509.18 -	419,268.25			
	<u>WATER RESOURCES</u>						
215	PAGLADIYA DAM PROJECT - [300100001	01/2001	542.90 -	1,187.00	12/2007 -	12/2012	118.64
	Total		542.90 -	420,455.25			
	Grand Total		237,406.02	3,224,886.19			

Details of Projects Without Milestones w.r.t. Original Schedule

			(September 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
1	GAGAN PROJECT - [N04000065]AAI,MULTI STATE	09/2008	626.00 -	06/2013 -	06/2013	0/0
2	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 335.61	05/2012 -	10/2014	0/0
3	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	03/2014 -	01/2015	0/0
4	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]AAI,CHANDIGARH	02/2011	452.00 -	03/2015 -	02/2015	0/0
5	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	03/2015 -	03/2016	0/0
6	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	01/2011 04/2013	12/2016	0/0
	Total		2,284.95 -			0/0
	<u>COAL</u>					
7	MURADIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	04/2014 -	04/2014	0/0
8	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	03/2014 -	03/2016	0/0
9	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND	08/2011	988.35 -	04/2017 -	04/2017	0/0
10	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05 -	03/2018 -	03/2018	0/0
11	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA	06/2014	289.03 -	03/2018 -	03/2018	0/0
12	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA	05/2014	479.15 -	03/2019 -	03/2019	0/0
13	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA	05/2014	337.66 -	03/2019 -	03/2019	0/0
14	MOONIDH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 2,500.00	04/2015 12/2018	04/2019	0/0
15	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL,CHHATISGARH	05/2014	164.49 -	03/2020 -	03/2020	0/0
16	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND	02/2014	555.52 -	03/2021 -	03/2021	0/0
17	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA	05/2014	3,756.36 -	03/2026 -	03/2026	0/0
	Total		9,349.58 -			0/0
	<u>PETROLEUM</u>					

			(September 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
18	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]BPCL,MAHARASHTRA	08/2009	246.81 276.83	08/2012 -	10/2014	0/0
19	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,ANDHRA PRADESH	01/2006	672.00 1,038.00	10/2011 -	12/2014	0/0
20	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL,ODISHA	07/2009	199.75 -	07/2013 -	12/2014	0/0
21	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]ONGC,MULTI STATE	10/2013	429.06 -	10/2014 -	12/2014	0/0
22	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,ASSAM	08/2008	144.02 204.29	06/2012 09/2013	12/2014	0/0
23	LPG MARKETING TERMINAL, PARADIP - [N16000174]IOCL,ODISHA	07/2009	158.91 -	03/2015 -	02/2015	0/0
24	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,MULTI STATE	08/2010	8,140.00 -	02/2014 -	03/2015	0/0
25	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	302.26 -	09/2012 -	03/2015	0/0
26	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 -	04/2015 -	04/2015	0/0
27	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC,MULTI STATE	04/2013	284.82 -	04/2015 -	04/2015	0/0
28	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,MULTI STATE	04/2003	429.82 3,955.21	04/2006 04/2016	06/2015	0/0
29	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 462.79	10/2014 -	10/2015	0/0
30	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	10/2011 -	10/2015	0/0
31	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA	01/2006	993.00 1,693.00	01/2012 -	10/2015	0/0
32	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	09/2011 -	12/2015	0/0
33	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	07/2015 -	12/2015	0/0
34	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	12/2012	607.06 -	01/2016 -	01/2016	0/0
35	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]ONGC,MAHARASHTRA	12/2012	3,513.07 -	02/2016 -	02/2016	0/0
36	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]IOCL,BIHAR	04/2013	480.00 -	02/2016 -	02/2016	0/0
37	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	12/2014 03/2016	03/2016	0/0
38	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE	05/2013	4,124.35 -	04/2016 -	04/2016	0/0
39	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL,KERALA	03/2012	14,225.00 16,504.00	05/2016 -	05/2016	0/0
40	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS - [N16000181]ONGC,MULTI STATE	03/2013	2,913.10 -	05/2016 -	05/2016	0/0
41	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	03/2013 -	06/2016	0/0

			(September 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
42	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]IOCL, ASSAM	02/2014	163.88 -	07/2016 -	07/2016	0/0
43	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL, GUJARAT	12/2011	160.00 -	03/2014 -	07/2016	0/0
44	GUJARAT REGION PIPELINE REPLACEMENT PROJECT - [N16000189]GAIL, GUJARAT	07/2014	716.00 -	01/2017 -	01/2017	0/0
45	KG BASIN PIPELINE REPLACEMENT PROJECT - [N16000190]GAIL, ANDHRA PRADESH	07/2014	762.00 -	01/2017 -	01/2017	0/0
46	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL, MULTI STATE	08/2006	94.00 352.56	09/2012 03/2017	03/2017	0/0
47	MH NORTH REDEVELOPMENT PHASE III - [N16000188]ONGC, MAHARASHTRA	06/2014	5,706.47 -	05/2017 -	05/2017	0/0
48	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL, WEST BENGAL	03/2014	3,076.00 -	09/2017 -	09/2017	0/0
49	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL, ODISHA	03/2014	3,150.00 -	09/2017 -	09/2017	0/0
50	AHMEDABAD REDEVELOPMENT PROJECT - [N16000120]ONGC, GUJARAT	11/2010	1,916.10 -	12/2014 -	12/2017	0/0
51	MEHESANA REDEVELOPMENT PROJECT - [N16000121]ONGC, GUJARAT	11/2010	3,823.00 -	04/2015 -	12/2017	0/0
52	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC, GUJARAT	11/2010	2,189.63 -	12/2014 -	12/2018	0/0
53	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]ONGC, MULTI STATE	03/2014	2,476.82 -	12/2018 -	12/2018	0/0
54	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL, MULTI STATE	07/2009	7,596.18 -	01/2013 -	02/2019	0/0
55	SURAT PARADIP PIPELINE PROJECT - [N16000163]GAIL, MULTI STATE	10/2012	10,281.00 -	04/2015 -	12/2020	0/0
56	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL, TAMIL NADU	05/2013	711.00 -	- -	-	0/0
57	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL, TAMIL NADU	11/2006	171.83 -	- -	-	0/0
58	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL, HARYANA	11/2007	281.07 -	10/2010 -	-	0/0
	Total		85,961.61 -			0/0
	<u>POWER</u>					
59	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL, MULTI STATE	03/2012	198.63 -	09/2014 -	09/2014	0/0
60	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]PGCIL, MULTI STATE	06/2012	1,909.24 -	06/2015 -	06/2015	0/0
61	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL, MULTI STATE	03/2014	155.57 -	03/2016 -	03/2016	0/0
62	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL, MULTI STATE	01/2014	374.63 -	04/2016 -	04/2016	0/0
63	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]PGCIL, MULTI STATE	05/2014	303.07 -	07/2016 -	07/2016	0/0

			(September 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
64	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE	05/2014	829.98 -	09/2016 -	09/2016	0/0
65	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 -	11/2016 -	11/2016	0/0
66	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE	08/2014	288.49 -	02/2017 -	02/2017	0/0
67	TRANS. SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]PGCIL,ANDHRA PRADESH	08/2014	188.75 -	02/2017 -	02/2017	0/0
68	TRANS. SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]PGCIL,MULTI STATE	06/2014	400.47 -	05/2017 -	05/2017	0/0
69	TRANS.SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	04/2018 -	04/2018	0/0
70	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	12/2018	0/0
71	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]PGCIL,JAMMU AND KASHMIR	10/2014	8,112.12 -	04/2020 -	04/2020	0/0
	Total		24,719.94 -			0/0
	<u>RAILWAYS</u>					
72	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	07/2008	0/0
73	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87 -	- 03/2010	03/2010	0/0
74	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	02/2012	0/0
75	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	02/2009 -	03/2012	0/0
76	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N22000052]WS&PU,BIHAR	04/2003	98.74 224.51	- -	03/2012	0/0
77	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,BIHAR	03/2005	470.09 1,417.97	- -	03/2012	0/0
78	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 03/2012	12/2012	0/0
79	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	611.03 -	12/2011 11/2013	11/2013	0/0
80	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- -	12/2013	0/0
81	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 -	- -	02/2014	0/0
82	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2014	0/0
83	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	02/2009 02/2009	08/2014	0/0
84	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	03/2009 03/2009	08/2014	0/0
85	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	03/1994 -	10/2014	0/0

			(September 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
86	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 236.41	- -	12/2014	0/0
87	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	12/2009 03/2011	12/2014	0/0
88	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 -	03/2009 12/2012	12/2014	0/0
89	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	09/2001	120.00 245.39	12/2008 -	12/2014	0/0
90	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	171.02 -	06/2013 -	12/2014	0/0
91	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	02/2015 -	02/2015	0/0
92	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,MULTI STATE	03/1984	520.00 835.04	03/1995 -	03/2015	0/0
93	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,062.36	- -	03/2015	0/0
94	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	03/2015	0/0
95	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	- 05/2009	03/2015	0/0
96	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,UTTAR PRADESH	03/2002	863.23 -	- -	03/2015	0/0
97	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]NEFR,ASSAM	01/2004	915.70 -	- -	03/2015	0/0
98	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	- -	03/2015	0/0
99	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	03/2012 12/2013	03/2015	0/0
100	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	03/2015 -	03/2015	0/0
101	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00 -	- -	03/2015	0/0
102	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 -	03/2015 -	03/2015	0/0
103	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	98.74 -	- -	03/2015	0/0
104	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	03/2015 -	03/2015	0/0
105	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	06/2004 -	12/2015	0/0
106	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 -	10/2007 12/2012	12/2015	0/0
107	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	261.70 -	02/2006 -	12/2015	0/0
108	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	03/2010 -	12/2015	0/0
109	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	401.81 495.44	03/2004 12/2010	03/2016	0/0

			(September 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
110	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266] NEFR, MULTI STATE	04/2000	733.00 733.00	12/2008 -	03/2016	0/0
111	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII-MUSORE (SWR) - [N22000107] SWR, KARNATAKA	04/2007	482.00 -	03/2013 -	03/2016	0/0
112	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109] RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	03/2016	0/0
113	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110] RVNL, WEST BENGAL	04/2010	3,951.98 4,259.48	03/2016 -	03/2016	0/0
114	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111] RVNL, WEST BENGAL	04/2010	2,913.51 -	03/2016 -	03/2016	0/0
115	KATAKHAL TO BHAIRABI - [N22000126] NEFR, ASSAM	04/1998	227.90 -	12/2012 -	03/2016	0/0
116	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127] NEFR, ASSAM	04/1996	1,676.31 -	03/2009 -	03/2016	0/0
117	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135] MRT, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	03/2016	0/0
118	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164] SER, JHARKHAND	04/2010	309.44 -	12/2015 -	03/2016	0/0
119	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194] NEFR, TRIPURA	04/1999	895.00 -	03/2007 -	03/2016	0/0
120	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214] MRT, MAHARASHTRA	04/2012	714.10 -	04/2016 -	04/2016	0/0
121	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108] RVNL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	06/2016	0/0
122	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162] SER, ODISHA	04/2010	149.90 -	03/2015 -	12/2016	0/0
123	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323] SER, JHARKHAND	04/2012	148.77 -	12/2016 -	12/2016	0/0
124	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086] NEFR, ASSAM	09/2006	200.00 -	- -	03/2017	0/0
125	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088] NR, UTTAR PRADESH	04/2006	325.00 -	03/2010 03/2017	03/2017	0/0
126	NEW COOCHBEHAR TO SAMUKTALA - [N22000197] NEFR, WEST BENGAL	04/2011	209.77 -	- -	03/2017	0/0
127	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198] NEFR, WEST BENGAL	04/2012	283.55 -	- -	03/2017	0/0
128	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210] NEFR, ASSAM	04/2011	312.12 -	- -	03/2017	0/0
129	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239] ER, MULTI STATE	04/2011	299.60 -	03/2017 -	03/2017	0/0
130	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245] ER, MULTI STATE	04/2010	423.66 -	03/2017 -	03/2017	0/0
131	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES, NEFR - [220100201] NEFR, ASSAM	09/1997	1,500.00 -	04/2008 03/2014	06/2017	0/0
132	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165] SER, JHARKHAND	04/2012	258.20 -	- -	12/2017	0/0
133	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288] NEFR, MANIPUR	04/2003	727.56 727.56	03/2011 03/2014	03/2018	0/0

			(September 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
134	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,TRIPURA	04/2008	813.34 -	03/2014 -	03/2018	0/0
135	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP,TELANGANA	04/2012	632.68 -	04/2012 03/2016	03/2018	0/0
136	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	11/2002 -	12/2018	0/0
137	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 2,030.50	02/2019 -	02/2019	0/0
138	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 6,213.84	03/2014 03/2019	03/2019	0/0
139	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 3,845.60	02/2020 -	02/2020	0/0
140	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,MIZORAM	04/2008	619.34 -	04/2014 03/2020	03/2020	0/0
141	SEVOK RANGPO, NEFR - [N22000102]NEFR,SIKKIM	04/2008	1,339.48 -	12/2015 -	03/2020	0/0
142	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NEFR,NAGALAND	04/2006	850.00 -	03/2015 03/2020	03/2020	0/0
143	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-	0/0
144	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	- 09/2009	-	0/0
145	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-	0/0
146	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-	0/0
147	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	03/2010 -	-	0/0
148	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR(221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	- -	-	0/0
149	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 -	- 03/2010	-	0/0
150	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 663.01	06/1999 -	-	0/0
151	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NEFR,WEST BENGAL	04/1983	36.80 274.41	- -	-	0/0
152	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	12/2011 12/2010	-	0/0
153	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	- -	-	0/0
154	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 -	- -	-	0/0
155	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	- -	-	0/0
156	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,038.00	03/1998 -	-	0/0
157	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	37.68 -	07/2012 -	-	0/0

			(September 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
158	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-	0/0
159	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	- -	-	0/0
160	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	2,957.21 -	07/2005 -	-	0/0
161	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	05/2008 -	-	0/0
162	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 335.77	03/2012 -	-	0/0
163	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,BIHAR	09/2001	492.98 -	12/2010 -	-	0/0
164	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	- -	-	0/0
165	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-	0/0
166	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-	0/0
167	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 -	- -	-	0/0
168	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	- -	-	0/0
169	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL	03/2000	1,049.69 3,156.32	12/2006 -	-	0/0
170	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	02/2011 02/2011	-	0/0
171	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	- 12/2009	-	0/0
172	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-	0/0
173	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	02/1999	138.00 -	- -	-	0/0
174	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,WEST BENGAL	03/1998	111.90 1,039.29	03/2005 12/2008	-	0/0
175	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	- -	-	0/0
176	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-	0/0
177	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-	0/0
178	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-	0/0
179	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-	0/0
180	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	470.92 727.13	- -	-	0/0
181	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	- -	-	0/0

			(September 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
182	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	- -	-	0/0
183	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	- -	-	0/0
184	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]JECR,BIHAR	04/1996	332.92 332.92	03/2012 -	-	0/0
185	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	06/2013 06/2013	-	0/0
186	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	378.56 -	- -	-	0/0
187	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	- -	-	0/0
188	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,MULTI STATE	12/2006	170.00 -	03/2011 -	-	0/0
189	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 -	- -	-	0/0
190	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 -	- -	-	0/0
191	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NEFR,BIHAR	09/2006	300.00 -	- -	-	0/0
192	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	1,106.62 -	12/2010 -	-	0/0
193	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 -	06/2005 07/2011	-	0/0
194	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,BIHAR	04/2008	282.92 -	- -	-	0/0
195	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	03/2014 -	-	0/0
196	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 -	03/2014 -	-	0/0
197	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	-	0/0
198	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER,WEST BENGAL	04/2009	259.51 -	12/2011 -	-	0/0
199	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER,WEST BENGAL	04/2004	293.74 -	12/2010 -	-	0/0
200	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 -	12/2012 -	-	0/0
201	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-	0/0
202	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	03/2013 -	-	0/0
203	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	03/2014 -	-	0/0
204	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	-	0/0
205	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-	0/0

			(September 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
206	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0
207	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	-	0/0
208	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	-	0/0
209	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	- -	-	0/0
210	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	- -	-	0/0
211	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
212	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	- -	-	0/0
213	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-	0/0
214	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	- -	-	0/0
215	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	- -	-	0/0
216	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	- -	-	0/0
217	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-	0/0
218	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 -	- -	-	0/0
219	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT	04/2013	1,266.89 -	- -	-	0/0
220	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	- -	-	0/0
221	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	- -	-	0/0
222	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2012	2,082.75 -	- -	-	0/0
223	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	-	0/0
224	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-	0/0
225	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0
226	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	- -	-	0/0
227	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	- -	-	0/0
228	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	- -	-	0/0
229	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	- -	-	0/0

			(September 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
230	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	- -	-	0/0
231	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	- -	-	0/0
232	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- -	-	0/0
233	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 -	- -	-	0/0
234	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	- -	-	0/0
235	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	- -	-	0/0
236	NAWADA-LAXMIPUR (NL) - [N22000167]SER,BIHAR	04/2008	620.57 -	- -	-	0/0
237	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-	0/0
238	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-	0/0
239	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-	0/0
240	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-	0/0
241	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-	0/0
242	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-	0/0
243	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-	0/0
244	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-	0/0
245	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-	0/0
246	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-	0/0
247	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-	0/0
248	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-	0/0
249	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-	0/0
250	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-	0/0
251	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-	0/0
252	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NEFR,MULTI STATE	04/2013	1,798.00 -	- -	-	0/0
253	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	- -	-	0/0

			(September 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
254	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-	0/0
255	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-	0/0
256	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-	0/0
257	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1999	271.24 -	- -	-	0/0
258	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	- -	-	0/0
259	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-	0/0
260	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-	0/0
261	NEW BG LINE FROM DUDHNOI-MENDIPATAR - [N22000192]NEFR,MULTI STATE	04/1999	175.43 -	- -	-	0/0
262	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NEFR,WEST BENGAL	04/2010	221.42 -	- -	-	0/0
263	AGARTALA-AKHAURA NL - [N22000195]NEFR,TRIPURA	04/2012	252.00 -	- -	-	0/0
264	DIMAPUR-TIZIT NL - [N22000196]NEFR,NAGALAND	04/2013	4,274.00 -	- -	-	0/0
265	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-	0/0
266	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-	0/0
267	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-	0/0
268	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-	0/0
269	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NEFR,MEGHALAYA	04/2010	4,083.02 -	- -	-	0/0
270	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NEFR,MULTI STATE	04/2010	242.22 -	- -	-	0/0
271	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NEFR,MULTI STATE	04/2010	241.52 -	- -	-	0/0
272	MURKONGSELEK-PASIGHAT NL - [N22000208]NEFR,MULTI STATE	04/2011	165.82 -	- -	-	0/0
273	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJBHATHKHOWA-JAI - [N22000209]NEFR,MULTI STATE	04/1999	523.17 -	- -	-	0/0
274	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NEFR,ASSAM	04/2012	246.07 -	- -	-	0/0
275	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSHUPUR - [N22000212]MRTP,WEST BENGAL	04/2009	573.78 -	- -	-	0/0
276	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-	0/0
277	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1999	406.99 -	- -	-	0/0

			(September 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
278	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-	0/0
279	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-	0/0
280	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-	0/0
281	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-	0/0
282	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-	0/0
283	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-	0/0
284	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-	0/0
285	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-	0/0
286	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-	0/0
287	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-	0/0
288	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-	0/0
289	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-	0/0
290	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	- -	-	0/0
291	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-	0/0
292	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-	0/0
293	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-	0/0
294	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-	0/0
295	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-	0/0
296	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-	0/0
297	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-	0/0
298	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-	0/0
299	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-	0/0
300	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-	0/0
301	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	182.06 -	- -	-	0/0

			(September 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
302	SANTOSH PUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-	0/0
303	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGREGATION OF ARRIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-	0/0
304	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-	0/0
305	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	96.16 -	- -	-	0/0
306	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-	0/0
307	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-	0/0
308	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	- -	-	0/0
309	MANUGURU-RAMAGUNDAM - [N22000259]SCOR,TELANGANA	04/2013	1,112.00 -	- -	-	0/0
310	KONDAPALLI-PENUBALLI - [N22000260]SCOR,MULTI STATE	04/2013	723.00 -	- -	-	0/0
311	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCOR,MULTI STATE	04/2012	1,054.35 -	- -	-	0/0
312	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCOR,MULTI STATE	04/2008	184.26 -	- -	-	0/0
313	BHADRACHALAM-KOVVUR - [N22000264]SCOR,MULTI STATE	04/2012	923.23 -	- -	-	0/0
314	GUDUR-DURGARAJAPATNAM - [N22000265]SCOR,ANDHRA PRADESH	04/2011	283.54 -	- -	-	0/0
315	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-	0/0
316	MANSABHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-	0/0
317	GRADE SEPARATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-	0/0
318	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-	0/0
319	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-	0/0
320	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-	0/0
321	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-	0/0
322	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-	0/0
323	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	-	0/0
324	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-	0/0
325	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-	0/0

			(September 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
326	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	- -	-	0/0
327	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-	0/0
328	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-	0/0
329	CUMBUM-PRODDATUR - [N22000282]SCOR,ANDHRA PRADESH	04/2013	829.00 -	- -	-	0/0
330	MUDKHED-PARBHANI - [N22000283]SCOR,MAHARASHTRA	04/2011	390.60 -	- -	-	0/0
331	NADIKUDE-SRI KALAHASTI - [N22000286]SCOR,ANDHRA PRADESH	04/2011	1,313.48 -	- -	-	0/0
332	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCOR,MULTI STATE	04/2010	337.49 -	- -	-	0/0
333	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	- -	11/2014	0/0
334	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-	0/0
335	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-	0/0
336	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-	0/0
337	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-	0/0
338	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-	0/0
339	UNCHAHAAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-	0/0
340	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-	0/0
341	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-	0/0
342	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	- -	-	0/0
343	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-	0/0
344	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	- -	-	0/0
345	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	-	0/0
346	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-	0/0
347	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-	0/0
348	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	01/1999 -	-	0/0
349	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 -	-	0/0

			(September 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
350	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-	0/0
351	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	01/1999 -	-	0/0
352	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-	0/0
353	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 -	- -	-	0/0
354	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 -	- -	-	0/0
355	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	- -	-	0/0
356	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 -	- -	-	0/0
357	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	- -	-	0/0
358	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-	0/0
359	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR,TAMIL NADU	04/2011	190.10 -	- -	-	0/0
360	HOSADURGA - CHICKAJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA	04/2010	203.40 -	- -	-	0/0
	Total		162,848.80 -			0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
361	PUNE-SHOLAPUR,PKG1 - [N24000127]NHAI,MAHARASHTRA	11/2009	1,110.00 -	05/2012 -	03/2012	0/0
362	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	07/2012 -	07/2012	0/0
363	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	12/2012 -	12/2012	0/0
364	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	01/2013 -	01/2013	0/0
365	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	02/2013 -	02/2013	0/0
366	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	05/2013	0/0
367	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA	02/2010	390.56 -	02/2012 -	06/2013	0/0
368	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	09/2013 -	09/2013	0/0
369	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	11/2013	0/0
370	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	11/2013	0/0
371	2 LANING OF MUZAFFARPUR - SONBARSA - [N24000174]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	11/2013	0/0

			(September 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
372	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	02/2014 -	02/2014	0/0
373	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	02/2014 -	02/2014	0/0
374	2LANING WITH PS GOPALGANJ-CHAPPRA - [N24000190]NHAI,BIHAR	12/2011	325.00 -	05/2014 -	05/2014	0/0
375	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	09/2014	0/0
376	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	07/2012 -	09/2014	0/0
377	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 01/2015	10/2014	0/0
378	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	10/2014	0/0
379	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00 -	10/2014 -	10/2014	0/0
380	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH	10/2012	250.50 -	10/2014 -	10/2014	0/0
381	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]NHAI,MADHYA PRADESH	10/2011	1,565.00 -	10/2014 -	10/2014	0/0
382	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	10/2008 -	11/2014	0/0
383	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	07/2013 -	11/2014	0/0
384	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	11/2014	0/0
385	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	11/2014	0/0
386	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	07/2014 -	11/2014	0/0
387	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN	03/2012	333.51 -	09/2014 -	11/2014	0/0
388	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 157.47	09/2007 03/2014	12/2014	0/0
389	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	09/2008 -	12/2014	0/0
390	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	12/2014	0/0
391	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	12/2014	0/0
392	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	04/2009 -	12/2014	0/0
393	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	09/2008 -	12/2014	0/0
394	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	10/2008 -	12/2014	0/0
395	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	04/2008 01/2015	12/2014	0/0

			(September 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
396	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	06/2008 -	12/2014	0/0
397	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	04/2008 01/2015	12/2014	0/0
398	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	04/2008 04/2015	12/2014	0/0
399	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 04/2015	12/2014	0/0
400	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 331.23	07/2009 -	12/2014	0/0
401	NH CONNECTIVITY TO ICTT VALLARPADA NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	02/2010 -	12/2014	0/0
402	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	12/2014	0/0
403	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	05/2012 -	12/2014	0/0
404	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	10/2011 -	12/2014	0/0
405	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	12/2014	0/0
406	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	03/2013 -	12/2014	0/0
407	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	12/2014	0/0
408	AMRITSAR-PATHANKOT - [N24000147]NHAI,PUNJAB	05/2010	705.00 -	11/2012 -	12/2014	0/0
409	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	11/2012 -	12/2014	0/0
410	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	12/2014	0/0
411	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	12/2014	0/0
412	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	12/2014	0/0
413	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	12/2014	0/0
414	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	12/2014	0/0
415	TWO LANNING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	12/2014	0/0
416	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	03/2013 -	12/2014	0/0
417	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	01/2014 -	12/2014	0/0
418	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	12/2014	0/0
419	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	12/2014	0/0

			(September 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
420	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	12/2014	0/0
421	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	05/2014 -	12/2014	0/0
422	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	08/2013 -	12/2014	0/0
423	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	06/2014 -	12/2014	0/0
424	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19 -	10/2014 -	12/2014	0/0
425	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	02/2015	0/0
426	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	03/2015	0/0
427	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	06/2008 -	03/2015	0/0
428	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	06/2008 -	03/2015	0/0
429	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 04/2015	03/2015	0/0
430	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 333.83	09/2007 -	03/2015	0/0
431	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	09/2010 -	03/2015	0/0
432	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	03/2015	0/0
433	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	06/2013 -	03/2015	0/0
434	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	12/2013 -	03/2015	0/0
435	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	03/2015	0/0
436	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	03/2015	0/0
437	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	01/2014 -	03/2015	0/0
438	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	08/2013 -	03/2015	0/0
439	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	07/2014 -	03/2015	0/0
440	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	04/2015 -	04/2015	0/0
441	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	05/2015	0/0
442	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	04/2014 -	05/2015	0/0
443	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	06/2005 -	06/2015	0/0

			(September 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
444	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	06/2015	0/0
445	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	09/2007 -	06/2015	0/0
446	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	10/2011 -	06/2015	0/0
447	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	06/2015	0/0
448	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	08/2013 -	06/2015	0/0
449	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,MULTI STATE	12/2012	1,479.00 -	06/2015 -	06/2015	0/0
450	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	07/2015	0/0
451	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00 -	08/2015 -	08/2015	0/0
452	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	02/2014 -	09/2015	0/0
453	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	09/2015	0/0
454	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	10/2015	0/0
455	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA	10/2013	283.25 -	10/2015 -	10/2015	0/0
456	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	06/2014 -	11/2015	0/0
457	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	10/2013 -	11/2015	0/0
458	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	11/2015 -	11/2015	0/0
459	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	12/2015	0/0
460	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	12/2015	0/0
461	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014 -	12/2015	0/0
462	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	01/2013 -	12/2015	0/0
463	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	12/2015	0/0
464	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	12/2015	0/0
465	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	08/2013 -	12/2015	0/0
466	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	12/2015	0/0
467	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	07/2014 -	12/2015	0/0

			(September 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
468	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	10/2013 -	12/2015	0/0
469	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	06/2014 -	12/2015	0/0
470	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	04/2010 01/2016	01/2016	0/0
471	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	02/2015 -	02/2016	0/0
472	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	03/2016	0/0
473	NASHRI CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	06/2010	2,159.00 -	06/2015 -	05/2016	0/0
474	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	06/2016	0/0
475	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	02/2010 -	07/2016	0/0
476	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	09/2016 -	09/2016	0/0
477	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	11/2016	0/0
478	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	09/2013 -	12/2016	0/0
479	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	01/2014 -	12/2016	0/0
480	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	10/2008 -	-	0/0
481	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	07/2008 -	-	0/0
482	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-	0/0
483	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	- -	-	0/0
484	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI,ANDHRA PRADESH	09/2013	606.00 -	- -	-	0/0
485	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI,TELANGANA	04/2014	1,123.17 -	- -	-	0/0
	Total		91,141.35 -			0/0
	<u>SHIPPING AND PORTS</u>					
486	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 298.17	04/2009 11/2009	02/2011	0/0
487	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY VESSELS - [N25000014]SHIPP.,MAHARASHTRA	10/2007	359.44 -	04/2011 11/2011	11/2011	0/0
488	MODIFICATION & STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST,GUJARAT	06/2010	277.00 -	03/2012 -	03/2012	0/0
489	ACQUISITION OF TWO NOS. OF 3060 DWT - [N25000043]SHIPP.,MAHARASHTRA	04/2009	277.03 280.00	12/2011 10/2012	10/2012	0/0

			(September 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
490	MECHANIZATION OF COAL HANDLING FACILITIES TO 200000 DWT VESSELS ON DBFOT BASIS - [N25000049]PORT TRUST,ANDHRA PRADESH	02/2010	444.10 -	06/2010 -	11/2012	0/0
491	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST - [N25000037]PORT TRUST,GUJARAT	04/2005	882.00 -	02/2011 -	12/2012	0/0
492	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,GUJARAT	12/2005	702.00 -	03/2011 -	03/2013	0/0
493	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST,GUJARAT	02/2011	830.00 -	05/2013 -	05/2013	0/0
494	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,MULTI STATE	07/2011	220.49 -	01/2013 06/2013	06/2013	0/0
495	ACQUISITION OF 4 NOS OF 82000 DWT KAMSAVMAX BULK CARRIERS FROM M/S JIANGSU EASTERN HEAVY INDUSTRIES - [N25000051]SHIPP.,MAHARASHTRA	08/2010	612.72 532.83	12/2012 11/2013	11/2013	0/0
496	ACQUISITION OF THREE(3) NOS OF 6500TEU CELLULAR CONTAINER VESSELS FROM M/S STX SHIPBUILDING CO. LTD. - [N25000052]SHIPP.,MAHARASHTRA	10/2010	1,028.10 1,012.23	12/2013 11/2013	11/2013	0/0
497	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 309.00	03/2006 06/2014	06/2014	0/0
498	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY - [N25000062]SHIPP.,MULTI STATE	01/2012	511.87 -	03/2014 08/2014	08/2014	0/0
499	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053]SHIPP.,MAHARASHTRA	10/2010	966.46 -	02/2014 01/2015	01/2015	0/0
500	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 1,460.00	12/2010 09/2012	03/2015	0/0
501	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 11/2010	-	0/0
502	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL - [N25000003]PORT TRUST,MAHARASHTRA	10/2005	800.00 1,571.60	10/2008 -	-	0/0
	Total		11,962.28 -			0/0
	<u>TELECOMMUNICATIONS</u>					
503	SUPPLY INSTALLATION TESTING AND COMMISSIONING OF RURAL WIMAX NETWORK PHASE-II - [N260000100]BSNL,MULTI STATE	07/2010	1,148.19 -	05/2011 -	06/2014	0/0
504	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTARANCHAL - [N26000058]BSNL,UTTARAKHAND	01/2009	149.15 -	06/2009 -	12/2014	0/0
505	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL,ASSAM	06/2007	336.81 -	01/2009 -	12/2014	0/0
506	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	10/2010 11/2015	03/2015	0/0
	Total		2,018.15 -			0/0
	<u>URBAN DEVELOPMENT</u>					
507	C/O MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	10/2012 -	09/2013	0/0
508	C/O MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB - [N28000070]CPWD,PUNJAB	08/2005	191.24 -	08/2007 -	12/2010	0/0
509	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI - [N28000064]CPWD,DELHI	01/2010	162.90 -	07/2012 -	07/2012	0/0

			(September 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
510	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]CPWD,BIHAR	02/2012	171.10 -	09/2014 -	09/2014	0/0
511	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA - [N28000078]CPWD,BIHAR	11/2006	2,727.89 -	03/2010 -	10/2014	0/0
512	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 -	11/2014 -	11/2014	0/0
513	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	03/2012 -	01/2015	0/0
514	FARIDABAD EXTENSION - [N28000057]DMRC,DELHI	09/2011	2,494.00 -	09/2014 -	05/2015	0/0
515	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD,WEST BENGAL	01/2009	225.81 -	06/2012 -	05/2015	0/0
516	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD,ODISHA	11/2012	238.43 -	02/2015 -	08/2015	0/0
517	C/O NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASHTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 -	06/2015 -	08/2015	0/0
518	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	11/2014 -	10/2015	0/0
519	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85 -	05/2013 -	10/2015	0/0
520	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	08/2014 -	01/2016	0/0
521	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	03/2016 -	03/2016	0/0
522	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI	05/2012	405.01 -	12/2014 -	04/2016	0/0
523	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	03/2016 -	05/2016	0/0
524	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	09/2016 -	09/2016	0/0
525	CONSTRUCTION OF CENTRAL ACADEMY FOR PUBLIC TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	12/2014 -	12/2016	0/0
526	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	09/2015 -	12/2016	0/0
527	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH	06/2014	157.84 -	03/2017 -	03/2017	0/0
528	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	07/2017 -	07/2017	0/0
529	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA	02/2014	26,405.14 -	02/2019 -	02/2019	0/0
530	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI - [N28000048]CPWD,MAHARASHTRA	11/2006	114.18 173.08	04/2009 -	-	0/0
	Total		76,291.31 -			0/0
	<u>WATER RESOURCES</u>					
531	PAGLADIYA DAM PROJECT - [300100001]MOWR,ASSAM	01/2001	542.90 -	12/2007 -	12/2012	0/0

			(September 2014)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	Total		542.90 -			0/0
	Grand Total		467,120.87			0/0

List of Projects on schedule w.r.t. Latest Schedule

							(September 2014)
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	9/2003	3,492.00 -	5,677.00	4,723.19	09/2010 03/2015	03/2015
	Total		3,492.00 -	5,677.00	4,723.19		
	<u>COAL</u>						
2	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]	6/2011	746.04 -	535.10	273.52	03/2015 -	03/2015
3	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]	12/2009	1,352.04 -	1,143.54	664.83	03/2016 03/2016	03/2016
4	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.00 -	490.10	183.63	03/2017 -	03/2017
5	BATURA OCP (2.0 MTY) - [N06000049]	9/2008	203.82 -	203.82	-	03/2015 -	03/2015
6	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	94.90	03/2016 -	03/2016
7	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) [N06000091]	6/2011	1,131.28 -	1,131.28	43.25	03/2018 -	03/2018
8	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]	4/2012	258.56 -	258.56	60.25	03/2016 -	03/2016
9	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	97.05	03/2020 -	03/2020
10	KULDA EXPN OC. (5.00 MTY) - [N06000115]	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
11	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]	5/2014	337.66 -	337.66	-	03/2019 -	03/2019
12	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	-	03/2026 -	03/2026
13	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]	5/2014	479.15 -	479.15	-	03/2019 -	03/2019
14	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	22.10	03/2020 -	03/2020
15	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]	8/2012	1,055.05 -	1,055.05	30.31	03/2018 -	03/2018
16	KAPURIA UG(PSLW) - [N06000108]	8/2011	988.35 -	988.35	6.84	04/2017 -	04/2017
17	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	6.84	03/2021 -	03/2021
18	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.33 -	610.33	-	03/2022 -	03/2022

(September 2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
19	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.14 -	430.14	68.08	03/2016 -	03/2016
20	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	7/2011	162.76 -	162.76	2.48	03/2015 -	03/2015
21	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]	12/2009	510.85 -	510.85	223.57	03/2016 -	03/2016
22	RKP OCP PHASE-I - [N06000079]	3/2010	209.78 -	209.78	68.51	03/2015 -	03/2015
23	PELMA OCP(10.00MTY) - [N06000045]	7/2008	448.32 -	448.32	0.46	03/2015 -	03/2015
	Total		15,188.23 -	14,816.89	1,846.62		
	<u>PETROLEUM</u>						
24	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]	3/2010	3,241.03 -	6,638.94	2,192.69	03/2013 11/2014	11/2014
25	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT [N16000129]	6/2009	2,915.00 -	2,300.00	1,408.97	12/2012 06/2015	06/2015
26	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	3/2012	14,225.00 -	16,504.00	3,483.53	05/2016 -	05/2016
27	KG BASIN PIPELINE REPLACEMENT PROJECT - [N16000190]	7/2014	762.00 -	762.00	-	01/2017 -	01/2017
28	GUJARAT REGION PIPELINE REPLACEMENT PROJECT - [N16000189]	7/2014	716.00 -	716.00	-	01/2017 -	01/2017
29	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	6/2014	5,706.47 -	5,706.47	-	05/2017 -	05/2017
30	RESID UPGRADATION PROJECT - [N16000184]	2/2011	3,110.36 -	3,110.36	242.84	11/2015 -	11/2015
31	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]	3/2014	2,476.82 -	2,476.82	-	12/2018 -	12/2018
32	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS - [N16000181]	3/2013	2,913.10 -	2,910.30	9.50	05/2016 -	05/2016
33	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY [N16000180]	2/2014	163.88 -	163.88	3.82	07/2016 -	07/2016
34	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00 -	3,150.00	92.49	09/2017 -	09/2017
35	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY [N16000177]	4/2013	480.00 -	480.00	3.02	02/2016 -	02/2016
36	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY [N16000175]	3/2014	3,076.00 -	3,076.00	42.24	09/2017 -	09/2017
37	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE [N16000173]	4/2013	284.82 -	284.82	-	04/2015 -	04/2015
38	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	5/2013	4,124.35 -	4,124.35	-	04/2016 -	04/2016

(September 2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
39	LPG TERMINAL AT KOCHI - [N16000171]	12/2012	607.06 -	607.06	47.38	01/2016 -	01/2016
40	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	8/2006	94.00 -	352.56	10.60	09/2012 03/2017	03/2017
41	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	9/2012	871.35 -	1,200.00	55.28	03/2015 11/2015	11/2015
42	GAS TURBINE GENERATION SET - [N18000146]	7/2009	216.88 -	216.88	186.44	10/2011 12/2014	12/2014
43	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]	4/2010	270.00 -	270.00	-	12/2014 03/2016	03/2016
44	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]	3/2013	1,138.50 -	1,138.50	145.86	04/2015 -	04/2015
45	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]	12/2012	3,513.07 -	3,513.07	0.27	02/2016 -	02/2016
46	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]	9/2011	202.25 -	160.16	36.33	07/2016 -	07/2016
47	MOUNDED BULLET PROJECT AT CPCL - [N16000154]	12/2012	279.00 -	279.00	95.32	12/2014 -	12/2014
48	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]	8/2011	586.00 -	586.00	198.47	08/2015 -	08/2015
49	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	2/2012	666.00 -	701.00	312.24	11/2015 -	11/2015
50	REWARI KANPUR PIPELINE PROJECT - [N16000145]	2/2012	1,210.64 -	1,210.64	732.58	11/2015 -	11/2015
51	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]	3/2012	5,608.40 -	5,608.40	2,805.04	05/2015 -	05/2015
	Total		62,607.98 -	68,247.21	12,104.91		
	<u>POWER</u>						
52	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	4,653.95	3,241.37	12/2009 03/2017	03/2017
53	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION [N18000123]	3/2012	198.63 -	198.63	-	09/2014 -	09/2014
54	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]	2/2012	1,927.16 -	1,927.16	-	10/2014 -	10/2014
55	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]	2/2012	1,310.85 -	1,310.85	-	02/2015 -	02/2015
56	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID [N18000130]	6/2012	1,263.26 -	1,263.26	-	11/2014 -	11/2014
57	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI [N18000136]	9/2012	803.34 -	803.34	379.39	03/2015 -	03/2015

(September 2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
58	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139	1/2013	182.80 -	182.80	76.33	10/2014 -	10/2014
59	TRANS.SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168	6/2014	5,151.37 -	5,151.37	-	04/2018 -	04/2018
60	TRANS. SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167	6/2014	400.47 -	400.47	-	05/2017 -	05/2017
61	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3&4 - [N18000166	2/2014	378.71 -	378.71	11.20	10/2016 -	10/2016
62	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165	3/2014	155.57 -	155.57	-	03/2016 -	03/2016
63	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164	5/2014	522.29 -	522.29	-	11/2016 -	11/2016
64	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163	5/2014	303.07 -	303.07	-	07/2016 -	07/2016
65	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162	5/2014	829.98 -	829.98	-	09/2016 -	09/2016
66	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161	2/2014	167.40 -	167.40	-	12/2015 -	12/2015
67	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160	2/2014	243.53 -	243.53	-	08/2016 -	08/2016
68	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172	10/2014	8,112.12 -	8,112.12	-	04/2020 -	04/2020
69	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171	2/2014	196.58 -	196.58	-	02/2016 -	02/2016
70	TRANS. SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170	8/2014	188.75 -	188.75	-	02/2017 -	02/2017
71	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169	8/2014	288.49 -	288.49	-	02/2017 -	02/2017
72	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159	2/2014	908.08 -	908.08	-	06/2016 -	06/2016
73	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158	2/2014	539.82 -	539.82	-	06/2016 -	06/2016
74	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157	1/2014	374.63 -	374.63	-	04/2016 -	04/2016
75	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153	9/2013	1,575.30 -	1,575.30	-	05/2016 -	05/2016
76	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152	9/2013	680.69 -	680.69	-	03/2016 -	03/2016

(September 2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
77	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]	6/2012	1,909.24 -	1,909.24	598.63	06/2015 -	06/2015
78	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]	3/2013	2,514.88 -	2,514.88	237.85	12/2015 -	12/2015
79	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	3/2013	514.20 -	514.20	-	06/2015 -	06/2015
80	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]	12/2012	156.04 -	156.04	-	10/2014 -	10/2014
81	VINDHYACHAL STPP STAGE-V - [N18000134]	12/2011	3,180.40 -	3,180.40	1,234.00	08/2015 -	08/2015
	Total		37,474.55 -	39,631.60	5,778.77		
	<u>RAILWAYS</u>						
82	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	4/1998	183.23 -	818.29	-	02/2015 -	02/2015
83	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	4/2006	325.00 -	1,116.53	374.71	03/2010 03/2017	03/2017
84	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	4/2008	5,300.00 -	7,012.84	1,820.40	03/2014 03/2019	03/2019
85	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	4/2010	3,951.98 -	4,259.48	733.02	03/2016 -	03/2016
86	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]	4/2008	829.74 -	829.74	75.09	03/2015 -	03/2015
87	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	3/2013	4,874.58 -	4,874.58	1,741.00	03/2016 -	03/2016
88	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	4/2012	148.77 -	174.69	1.80	12/2016 -	12/2016
89	DELANG-PURI DOUBLING - [N22000320]	3/2011	165.16 -	165.16	106.62	03/2015 -	03/2015
90	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	4/2010	423.66 -	423.66	215.50	03/2017 -	03/2017
91	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	4/2011	299.60 -	299.60	1.10	03/2017 -	03/2017
92	PLASSEY-JIAGANJ DOUBLING - [N22000220]	4/2011	248.07 -	248.07	26.60	03/2015 -	03/2015
93	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]	4/2012	714.10 -	714.10	46.02	04/2016 -	04/2016
94	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANPUR- BANSI PAHARPUR - [N22000158]	4/2010	622.41 -	2,030.50	2.43	02/2019 -	02/2019
95	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	1,176.09 -	3,845.60	1.92	02/2020 -	02/2020

(September 2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
96	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	4/2006	850.00 -	2,446.57	10.23	03/2015 03/2020	03/2020
97	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	4/2010	2,913.51 -	2,913.51	382.68	03/2016 -	03/2016
98	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	4/2008	619.34 -	2,393.48	192.81	04/2014 03/2020	03/2020
	Total		23,645.24 -	34,566.40	5,731.93		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
99	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	258.40	04/2010 01/2016	01/2016
100	PANIPAT-ROHTAK - [N24000151]	4/2011	807.00 -	807.00	1,209.43	10/2014 -	10/2014
101	RANCHI-RARGA-JAMSETHPUR - [N24000215]	12/2012	1,479.00 -	1,479.00	354.70	06/2015 -	06/2015
102	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	919.30	09/2015 -	09/2015
103	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	150.20	12/2015 -	12/2015
104	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	4/2014	1,266.60 -	1,266.60	-	09/2016 -	09/2016
105	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]	11/2013	1,916.79 -	1,916.79	273.20	11/2016 -	11/2016
106	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]	10/2013	283.25 -	283.25	218.70	10/2015 -	10/2015
107	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]	6/2013	1,287.95 -	1,287.95	540.10	11/2015 -	11/2015
108	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]	10/2011	1,565.00 -	1,565.00	1,556.00	10/2014 -	10/2014
109	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	1,928.22	642.90	04/2015 -	04/2015
110	2 LANING WITH PS AGRA ALIGARH - [N24000220]	10/2012	250.50 -	250.50	363.10	10/2014 -	10/2014
111	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]	2/2013	1,232.00 -	1,232.00	590.90	08/2015 -	08/2015
112	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]	4/2012	1,396.18 -	1,396.18	1,760.00	09/2014 -	09/2014
	Total		17,328.34 -	17,420.29	8,836.93		
	<u>SHIPPING AND PORTS</u>						

(September 2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
113	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053	10/2010	966.46 -	994.82	427.54	02/2014 01/2015	01/2015
	Total		966.46 -	994.82	427.54		
	<u>STEEL</u>						
114	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080	11/2012	313.05 -	313.05	135.24	06/2015 -	06/2015
115	REBUILDING OF COB-7 AT BSL - [N12000083	10/2013	245.67 -	245.67	18.01	05/2016 -	05/2016
116	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084	6/2014	708.91 -	708.91	1.79	04/2016 -	04/2016
117	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085	4/2014	188.93 -	188.93	-	04/2015 -	04/2015
	Total		1,456.56 -	1,456.56	155.04		
	<u>URBAN DEVELOPMENT</u>						
118	DELHI MRTS PHASE-III - [N28000056	9/2011	38,585.00 -	38,585.00	8,699.49	03/2016 -	03/2016
119	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058	2/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019
120	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060	4/2014	332.72 -	332.72	0.08	09/2016 -	09/2016
121	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063	2/2012	171.10 -	171.10	85.60	09/2014 -	09/2014
122	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068	2/2011	241.33 -	241.33	22.43	11/2014 -	11/2014
123	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 -	1,219.21	-	07/2017 -	07/2017
124	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076	6/2014	157.84 -	157.84	2.04	03/2017 -	03/2017
	Total		67,112.34 -	67,112.34	8,809.64		
	Grand Total		229,271.70	249,923.11	48,414.57		

List of Projects Ahead of Schedule w.r.t. Latest Schedule

(September 2014)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>PETROLEUM</u>						
1	DEV OF G1 AND GS-15 (ONGCL) - [160100231	4/2003	429.82 3,955.21	3,955.21	3,413.13	04/2006 04/2016	06/2015
	Total		429.82 -	3,955.21	3,413.13		
	<u>CIVIL AVIATION</u>						
2	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II [N04000070	2/2011	452.00 -	452.00	309.21	03/2015 -	02/2015
	Total		452.00 -	452.00	309.21		
	<u>POWER</u>						
3	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID [N16000144	9/2012	1,508.74 -	1,508.74	402.08	06/2016 -	12/2015
	Total		1,508.74 -	1,508.74	402.08		
	<u>PETROLEUM</u>						
4	KOTA JOBNER PIPELINE PROJECT - [N16000170	4/2011	276.26 -	276.27	174.81	12/2015 -	03/2015
5	LPG MARKETING TERMINAL, PARADIP - [N16000174	7/2009	158.91 -	158.91	113.85	03/2015 -	02/2015
6	RESITEMENT OF BILASPUR AND BISRAMPUR DEPOTS TO KORBA (CHATTISGARH) [N16000186	1/2011	141.86 219.08	219.08	93.99	09/2016 -	12/2015
	Total		577.03 -	654.26	382.65		
	<u>POWER</u>						
7	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119	1/2011	368.72 -	913.63	656.12	07/2006 12/2015	02/2015
8	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID [N18000137	9/2012	1,935.35 -	1,935.35	-	12/2014 -	11/2014
9	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) [N18000154	10/2013	1,315.90 -	1,315.90	-	11/2016 -	03/2016
10	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155	10/2013	1,364.52 -	1,364.52	-	05/2016 -	04/2016
	Total		4,984.49 -	5,529.40	656.12		

(September 2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
11	GUWHATI TO NALBARI (AS-4) - [N24000038]	12/2003	175.96 -	175.96	286.70	04/2008 01/2015	12/2014
12	SONAPUR TO GUWAHTI (AS-3) - [N24000044]	12/2003	245.00 -	245.00	491.20	03/2008 01/2015	10/2014
13	GUWAHATI TO NALBARI (AS-5) - [N24000046]	12/2003	198.16 -	198.16	341.00	04/2008 01/2015	12/2014
14	NALBARI TO BIJNI (AS-6) - [N24000047]	12/2003	225.00 -	225.00	276.40	06/2008 04/2015	03/2015
15	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 230.00	208.00	334.10	04/2008 04/2015	12/2014
16	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]	12/2003	160.00 -	160.00	211.70	05/2008 04/2015	12/2014
	Total		1,212.12 -	1,212.12	1,941.10		
	<u>TELECOMMUNICATIONS</u>						
17	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]	10/2009	384.00 -	384.00	48.95	10/2010 11/2015	03/2015
	Total		384.00 -	384.00	48.95		
	Grand Total		9,548.20	13,695.73	7,153.24		

List of Delayed Projects w.r.t. Latest Schedule

(September 2014)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00 17,270.00	17,270.00	17,894.00	12/2008 10/2013	11/2014	71	13
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	5,399.00	12/2015 11/2016	10/2017	22	11
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	3,294.00	12/2016 03/2017	05/2018	17	14
	Total		36,950.00 -	41,049.00	26,587.00				
	<u>CIVIL AVIATION</u>								
4	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 335.61	388.53	284.00	05/2012 -	10/2014	29	-
5	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	344.28	19.61	03/2014 -	01/2015	10	-
6	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	217.60	0.04	03/2015 -	03/2016	12	-
7	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	309.46	277.91	01/2011 04/2013	12/2016	71	44
	Total		1,206.95 -	1,259.87	581.56				
	<u>COAL</u>								
8	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,TAMIL NADU	10/2004	2,030.78 3,027.59	3,321.86	3,035.56	06/2009 03/2013	10/2014	64	19
9	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	5,632.17	03/2012 05/2014	11/2014	32	6
10	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]NLC,TAMIL NADU	04/2012	364.75 -	364.75	92.32	10/2014 -	11/2014	1	-
11	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 -	259.40	7.45	03/2012 -	03/2015	36	-
12	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	453.63	105.42	12/2012 -	03/2015	27	-
13	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	144.07	03/2013 -	03/2015	24	-
14	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,TELANGANA	12/2009	212.34 1,228.39	1,228.39	1,228.77	03/2013 09/2012	09/2015	30	36
15	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,583.65	03/2014 -	03/2016	24	-
16	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,560.52	03/2014 -	03/2016	24	-
17	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	469.78 -	706.40	44.65	07/2012 -	03/2016	44	-

(September 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
18	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35 -	462.35	273.00	03/2014 -	03/2016	24	-
19	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	42.46	03/2014 -	03/2016	24	-
20	PENGANGA OC - [N06000066]WCL,MAHARASHTRA	10/2008	339.77 -	339.77	1.69	03/2014 -	03/2016	24	-
21	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24	-
22	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	418.97	229.11	03/2012 -	03/2016	48	-
23	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	181.19	36.13	03/2012 -	03/2016	48	-
24	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.42 -	321.50	211.59	03/2014 -	03/2016	24	-
25	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	35.52	03/2011 -	03/2016	60	-
26	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	142.19	03/2012 -	03/2016	48	-
27	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	6.56	06/2015 -	06/2016	12	-
28	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	129.48	03/2010 -	03/2017	84	-
29	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	471.66 341.63	341.63	102.07	03/2011 -	03/2017	72	-
30	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL	11/2006	287.18 -	287.17	44.71	03/2011 -	03/2017	72	-
31	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	120.75	03/2013 -	03/2017	48	-
32	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	146.04	03/2010 -	03/2017	84	-
33	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	170.25	03/2012 -	03/2017	60	-
34	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.63 -	479.63	118.51	03/2013 -	03/2017	48	-
35	JAGANNATHPOR OC - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	152.43	21.55	03/2015 -	03/2017	24	-
36	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	60.93	03/2012 -	03/2017	60	-
37	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	55.96	03/2014 -	03/2017	36	-
38	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	417.33	2.22	07/2016 -	03/2017	8	-
39	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	242.29	0.30	03/2015 -	03/2018	36	-
40	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	447.06	29.03	03/2015 -	03/2018	36	-
41	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 -	5,907.11	371.49	12/2015 -	04/2018	28	-
42	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 2,500.00	1,230.27	1,000.00	04/2015 12/2018	04/2019	48	4
43	TALABIRA OCP - [N06000043]MCL,ODISHA	03/2008	447.72 -	447.72	52.34	03/2016 -	03/2020	48	-

(September 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
44	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL, ODISHA	02/2008	395.87 -	395.87	76.74	03/2015 -	03/2021	72	-
45	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL, CHHATISGARH	06/2008	1,188.31 -	7,612.33	755.52	03/2013 -	03/2023	120	-
	Total		29,523.97 -	40,059.98	17,670.72				
	<u>STEEL</u>								
46	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL, ANDHRA PRADESH	06/2006	108.00 216.68	216.68	164.85	09/2008 12/2013	10/2014	73	10
47	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL, ANDHRA PRADESH	10/2005	8,692.00 12,291.00	12,291.00	10,976.01	10/2009 10/2012	12/2014	62	26
48	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL, WEST BENGAL	06/2008	14,443.00 -	16,408.00	16,340.70	12/2011 -	12/2014	36	-
49	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL, JHARKHAND	05/2010	6,325.00 -	6,325.00	4,856.37	12/2011 -	12/2014	36	-
50	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHHATISGARH - [N12000078]SAIL, CHHATISGARH	07/2012	332.65 -	332.65	137.76	08/2014 -	01/2015	5	-
51	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL, ODISHA	10/2012	160.48 -	160.48	97.05	09/2014 -	01/2015	4	-
52	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]NMDC, CHHATISGARH	01/2007	295.89 607.17	607.17	376.30	12/2011 01/2015	03/2015	39	2
53	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]RINL, MULTI STATE	07/2007	480.00 -	450.00	322.07	09/2009 05/2012	03/2015	66	34
54	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]SAIL, ODISHA	08/2010	11,812.00 -	11,812.00	11,497.14	03/2013 -	03/2015	24	-
55	1.2 MTPA PELLET PLANT PROJECT, DONIMALAI (NMDC) - [N12000072]NMDC, KARNATAKA	04/2011	572.00 -	572.00	404.31	04/2013 09/2014	03/2015	23	6
56	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC, KARNATAKA	02/2011	898.55 -	898.55	343.43	05/2013 01/2015	03/2015	22	2
57	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL, WEST BENGAL	08/2010	2,875.00 -	2,875.00	2,355.92	12/2012 -	03/2015	27	-
58	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODISHA - [N12000079]SAIL, ODISHA	06/2012	237.09 -	237.09	87.87	12/2014 -	03/2015	3	-
59	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL, ODISHA	11/2011	254.55 -	254.55	114.35	11/2013 -	06/2015	19	-
60	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL, MAHARASHTRA	12/2011	187.33 -	187.33	138.60	10/2013 -	08/2015	22	-
61	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, CHHATISGARH	08/2010	17,265.00 -	17,265.00	13,392.35	03/2013 -	09/2015	30	-
	Total		64,938.54 -	70,892.50	61,605.08				
	<u>PETROLEUM</u>								
62	MRPL PHASE-III EXPANSION - [N16000114]MANGALORE REFIN, KARNATAKA	08/2008	12,412.00 -	12,160.26	-	01/2012 -	09/2014	32	-

(September 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
63	WAX PROJECT - [N16000101]NRL,ASSAM	06/2010	576.60 676.05	676.05	560.73	12/2013 05/2014	10/2014	10	5
64	POLYPROPYLENE UNIT - [N16000113]MANGALORE REFIN,KARNATAKA	05/2009	1,803.78 -	1,803.78	1,016.69	07/2012 -	10/2014	27	-
65	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]BPCL,MAHARASHTRA	08/2009	246.81 276.83	276.83	261.43	08/2012 -	10/2014	26	-
66	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,ANDHRA PRADESH	03/2009	3,597.00 2,730.00	2,730.00	3,128.58	09/2011 03/2012	11/2014	38	32
67	102 MW WIND POWER PROJECT - [N16000119]ONGC,RAJASTHAN	07/2010	1,106.00 -	678.02	405.00	06/2012 -	12/2014	30	-
68	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,ANDHRA PRADESH	01/2006	672.00 1,038.00	1,038.00	991.73	10/2011 -	12/2014	38	-
69	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL,ODISHA	07/2009	199.75 -	199.75	145.55	07/2013 -	12/2014	17	-
70	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]ONGC,MULTI STATE	10/2013	429.06 -	429.06	-	10/2014 -	12/2014	2	-
71	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,ASSAM	08/2008	144.02 204.29	204.29	155.04	06/2012 09/2013	12/2014	30	15
72	DABHOL BANGALORE PIPELINE PROJECT PHASE-II - [N16000147]GAIL,MULTI STATE	06/2009	486.00 -	486.00	107.14	09/2013 -	02/2015	17	-
73	PARADIP REFINERY PROJECT - [N16000058]IOCL,ODISHA	02/2009	29,777.00 34,555.00	34,555.00	26,919.64	11/2012 11/2013	03/2015	28	16
74	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]ONGC,TRIPURA	07/2008	288.04 288.04	253.66	216.68	08/2012 -	03/2015	31	-
75	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,MULTI STATE	08/2010	8,140.00 -	8,140.00	7,117.42	02/2014 -	03/2015	13	-
76	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	302.26 -	240.95	106.67	09/2012 -	03/2015	30	-
77	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 -	761.68	634.95	05/2013 06/2014	03/2015	22	9
78	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL,MAHARASHTRA	03/2012	1,419.00 -	1,419.00	771.67	12/2014 -	03/2015	3	-
79	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE	01/2012	352.49 -	352.49	99.82	03/2014 -	04/2015	13	-
80	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,MAHARASHTRA	06/2007	3,248.78 5,633.44	6,000.00	5,867.78	08/2010 03/2012	05/2015	57	38
81	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC,MULTI STATE	11/2010	331.20 -	269.10	190.04	08/2013 -	05/2015	21	-
82	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	598.34	03/2015 -	05/2015	2	-
83	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 -	2,592.17	310.34	05/2014 -	05/2015	12	-
84	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17 -	600.17	248.92	12/2014 -	05/2015	5	-
85	PIPELINE REPLACEMENT PROJECT-3 - [N16000137]ONGC,MULTI STATE	04/2012	2,547.26 -	1,417.00	1,304.57	05/2014 -	05/2015	12	-

(September 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
86	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	330.47	270.86	06/2011 03/2012	07/2015	49	40
87	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 462.79	462.79	94.94	10/2014 -	10/2015	12	-
88	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]JSPRL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	888.80	10/2011 -	10/2015	48	-
89	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]JSPRL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,283.65	01/2012 -	10/2015	45	-
90	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	736.65	469.52	09/2011 -	12/2015	51	-
91	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	1,019.33	09/2012 -	12/2015	39	-
92	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE	06/2010	2,523.00 -	2,523.00	1,013.04	01/2014 -	12/2015	23	-
93	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	913.00	326.01	07/2015 -	12/2015	5	-
94	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96 -	191.96	53.98	05/2015 -	12/2015	7	-
95	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 -	2,378.86	1,711.73	03/2013 03/2015	03/2016	36	12
96	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	723.64	-	03/2013 -	06/2016	39	-
97	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL,GUJARAT	12/2011	160.00 -	160.00	-	03/2014 -	07/2016	28	-
98	AHMEDABAD REDEVELOPMENT PROJECT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10 -	1,916.10	1,160.14	12/2014 -	12/2017	36	-
99	MEHESANA REDEVELOPMENT PROJECT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	3,823.00	1,076.57	04/2015 -	12/2017	32	-
100	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63 -	2,189.63	1,039.42	12/2014 -	12/2018	48	-
101	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18 -	7,596.18	13.50	01/2013 -	02/2019	73	-
102	SURAT PARADIP PIPELINE PROJECT - [N16000163]GAIL,MULTI STATE	10/2012	10,281.00 -	10,281.00	1.36	04/2015 -	12/2020	68	-
	Total		112,003.25 -	118,888.19	61,581.58				
	<u>POWER</u>								
103	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]PGCIL,MULTI STATE	08/2008	2,360.95 -	2,580.90	-	08/2012 -	09/2014	25	-
104	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118]PGCIL,GUJARAT	01/2012	259.28 -	259.28	169.82	01/2014 -	10/2014	9	-
105	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 623.44	994.85	833.58	07/2013 08/2014	11/2014	16	3

(September 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
106	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 -	2,074.86	1,657.94	03/2013 -	11/2014	20	-
107	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000107]PGCIL,CHHATISGARH	08/2011	1,391.97 -	1,391.97	-	12/2013 -	11/2014	11	-
108	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL,MADHYA PRADESH	03/2012	213.78 -	213.78	153.34	03/2014 -	11/2014	8	-
109	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 -	477.69	495.59	09/2010 -	12/2014	51	-
110	SYSTEM STRENGTHENING IN NR FOR SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,022.39	08/2012 -	12/2014	28	-
111	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	487.49	305.72	06/2014 -	12/2014	6	-
112	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	437.80	02/2014 -	12/2014	10	-
113	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19 -	2,743.19	2,368.80	12/2013 -	02/2015	14	-
114	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]PGCIL,MULTI STATE	03/2011	2,569.25 -	2,569.25	2,550.67	03/2014 -	02/2015	11	-
115	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]PGCIL,MULTI STATE	09/2011	1,366.34 -	1,366.34	1,123.46	12/2013 -	02/2015	14	-
116	BARH STPP STAGE -II - [N18000047]NTPC,BIHAR	02/2008	7,341.04 -	7,341.04	7,902.00	08/2013 -	03/2015	19	-
117	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. - [N18000076]PGCIL,MULTI STATE	03/2010	4,672.99 -	4,672.99	3,381.37	11/2012 -	03/2015	28	-
118	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 -	752.64	425.52	07/2013 -	03/2015	20	-
119	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATISGARH	05/2011	1,961.87 -	1,961.87	1,528.65	05/2014 -	03/2015	10	-
120	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,479.66	09/2014 -	03/2015	6	-
121	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	310.81	11/2013 -	03/2015	16	-
122	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH	11/2011	2,127.51 -	2,127.51	1,943.33	07/2014 -	03/2015	8	-

(September 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
123	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	412.62	11/2014 -	03/2015	4	-
124	KOLDAM HEP (NTPC) - [180100211]NTPC,HIMACHAL PRADESH	10/2002	4,527.15 7,220.00	7,220.00	6,077.00	04/2009 -	05/2015	73	-
125	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 -	1,746.65	570.83	08/2014 -	05/2015	9	-
126	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	142.92	04/2015 -	05/2015	1	-
127	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	9,188.20	08/2013 -	06/2015	22	-
128	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	1,867.60	12/2012 -	06/2015	30	-
129	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	-	01/2013 -	06/2015	29	-
130	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,319.96	11/2013 -	06/2015	19	-
131	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	1,216.96	08/2014 -	06/2015	10	-
132	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATISGARH	01/2012	1,422.85 -	1,422.85	799.32	01/2015 -	06/2015	5	-
133	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	-	10/2014 -	06/2015	8	-
134	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99 1,128.38	1,128.38	909.40	08/2013 -	09/2015	25	-
135	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	3,972.68	10/2012 -	12/2015	38	-
136	TRANSM SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B - [N18000077]PGCIL, WEST BENGAL	04/2010	4,404.57 -	4,404.57	661.15	01/2015 -	12/2015	11	-
137	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	892.43	11/2012 -	12/2015	37	-
138	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATISGARH	03/2012	9,569.76 -	9,569.76	-	06/2015 -	12/2015	6	-
139	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC, WEST BENGAL	09/2005	1,061.38 -	1,929.15	1,551.17	09/2009 -	03/2016	78	-
140	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	415.06	11/2011 -	03/2016	52	-

(September 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
141	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	694.44	11/2012 -	03/2016	40	-
142	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,086.62	04/2013 -	03/2016	35	-
143	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	6,749.18 6,749.18	6,749.18	4,726.00	07/2011 -	08/2016	61	-
144	KISHANGANGA HEP - [N18000031]NHPC,JAMMU AND KASHMIR	07/2007	3,642.04 3,642.04	5,497.72	3,644.34	01/2016 -	11/2016	10	-
145	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	12/2003	8,692.97 -	8,693.00	10,264.00	12/2009 -	03/2017	87	-
146	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	2,202.00	03/2013 -	03/2018	60	-
147	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	12/2011	15,166.19 -	15,166.19	5,031.00	12/2016 -	03/2018	15	-
148	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	7,921.47	3,051.00	09/2016 -	03/2018	18	-
149	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 2,998.00	9,395.18	3,102.00	11/2016 -	03/2018	16	-
150	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	1,527.00	140.00	08/2017 -	03/2018	7	-
151	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	02/2013	11,638.55 -	11,638.55	1,471.00	09/2017 -	03/2018	6	-
152	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	909.81	07/2010 02/2016	05/2018	94	27
153	PARBATI HEP (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	5,366.00	4,667.37	09/2009 -	07/2018	106	-
154	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,UTTARAKHAND	08/2008	2,491.58 3,745.08	3,745.08	498.11	07/2014 -	07/2018	48	-
155	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	6,285.33	6,943.84	09/2010 -	12/2018	99	-
156	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	11/2012	11,846.00 -	11,846.00	1,846.00	05/2017 -	03/2019	22	-
	Total		183,937.63 -	195,591.73	108,365.28				
	<u>RAILWAYS</u>								
157	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	608.02	593.82	03/1994 -	10/2014	247	-
158	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	432.72	414.84	12/2009 03/2011	12/2014	60	45
159	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 -	2,363.00	1,473.59	03/2009 12/2012	12/2014	69	24
160	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	09/2001	120.00 245.39	245.39	232.11	12/2008 -	12/2014	72	-
161	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	171.02 -	171.02	155.41	06/2013 -	12/2014	18	-

(September 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
162	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,MULTI STATE	03/1984	520.00 835.04	835.04	646.73	03/1995 -	03/2015	240	-
163	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	445.40	180.72	03/2007 03/2007	03/2015	96	96
164	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	272.39	141.55	03/2012 12/2013	03/2015	36	15
165	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	334.90	230.66	06/2004 -	12/2015	138	-
166	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 -	2,921.00	2,252.44	10/2007 12/2012	12/2015	98	36
167	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	261.70 -	261.70	156.22	02/2006 -	12/2015	118	-
168	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	800.00	798.47	03/2010 -	12/2015	69	-
169	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	401.81 495.44	1,814.10	392.88	03/2004 12/2010	03/2016	144	63
170	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NEFR,MULTI STATE	04/2000	733.00 733.00	2,483.04	1,673.08	12/2008 -	03/2016	87	-
171	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	874.57	606.09	03/2013 -	03/2016	36	-
172	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	2,298.42	78.05	03/2014 -	03/2016	24	-
173	KATAKHAL TO BHAIRABI - [N22000126]NEFR,ASSAM	04/1998	227.90 -	331.40	174.44	12/2012 -	03/2016	39	-
174	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NEFR,ASSAM	04/1996	1,676.31 -	5,185.44	4,452.04	03/2009 -	03/2016	84	-
175	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 -	388.67	111.16	12/2015 -	03/2016	3	-
176	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NEFR,TRIPURA	04/1999	895.00 -	1,242.25	994.65	03/2007 -	03/2016	108	-
177	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL,WEST BENGAL	04/2010	2,397.72 -	2,397.72	121.21	03/2016 -	06/2016	3	-
178	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	184.91	64.70	03/2015 -	12/2016	21	-
179	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]NEFR,ASSAM	09/1997	1,500.00 -	4,996.19	3,326.02	04/2008 03/2014	06/2017	110	39
180	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,MANIPUR	04/2003	727.56 727.56	5,996.00	2,519.80	03/2011 03/2014	03/2018	84	48
181	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,TRIPURA	04/2008	813.34 -	1,741.00	752.27	03/2014 -	03/2018	48	-
182	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP,TELANGANA	04/2012	632.68 -	816.55	17.42	04/2012 03/2016	03/2018	71	24
183	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	19,565.00	9,965.25	11/2002 -	12/2018	193	-

(September 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
184	SEVOK RANGPO, NEFR - [N22000102]NEFR,SIKKIM	04/2008	1,339.48 -	3,375.42	85.64	12/2015 -	03/2020	51	-
	Total		21,415.35 -	63,381.26	32,611.26				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
185	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	635.90	608.30	07/2012 -	09/2014	26	-
186	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	200.00	288.80	06/2008 -	10/2014	76	-
187	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	250.39	285.30	10/2008 -	11/2014	73	-
188	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	593.00	759.90	07/2013 -	11/2014	16	-
189	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	381.50	06/2013 -	11/2014	17	-
190	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	-	10/2013 -	11/2014	13	-
191	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	373.47	268.60	07/2014 -	11/2014	4	-
192	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN	03/2012	333.51 -	333.51	270.80	09/2014 -	11/2014	2	-
193	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 157.47	154.57	267.60	09/2007 03/2014	12/2014	87	9
194	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	201.66	191.70	09/2008 -	12/2014	75	-
195	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	280.00	366.10	02/2009 -	12/2014	70	-
196	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	167.64	138.80	11/2008 -	12/2014	73	-
197	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	200.00	207.20	04/2009 -	12/2014	68	-
198	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	332.94	525.80	09/2008 -	12/2014	75	-
199	RAJMARG CHORAH TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	251.03	384.70	10/2008 -	12/2014	74	-
200	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	264.72	315.70	06/2008 -	12/2014	78	-
201	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 331.23	363.74	240.40	07/2009 -	12/2014	65	-
202	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	557.00	1,123.00	02/2010 -	12/2014	58	-
203	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	666.40	05/2010 -	12/2014	55	-
204	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	1,509.10	2,613.00	09/2012 -	12/2014	27	-
205	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	795.00	1,132.00	05/2012 -	12/2014	31	-

(September 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
206	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	353.37	446.20	10/2011 -	12/2014	38	-
207	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	1,693.75	2,762.00	08/2011 -	12/2014	40	-
208	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	12/2014	20	-
209	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	899.70	03/2013 -	12/2014	21	-
210	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	996.80	05/2013 -	12/2014	19	-
211	AMRITSAR-PATHANKOT - [N24000147]NHAI,PUNJAB	05/2010	705.00 -	705.00	2,208.00	11/2012 -	12/2014	25	-
212	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	193.45	66.01	11/2012 -	12/2014	25	-
213	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,292.00	03/2013 -	12/2014	21	-
214	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	1,173.00	07/2013 -	12/2014	17	-
215	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	632.70	02/2013 -	12/2014	22	-
216	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	1,141.00	2,157.00	08/2013 -	12/2014	16	-
217	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,321.00	12/2013 -	12/2014	12	-
218	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	148.80	05/2013 -	12/2014	19	-
219	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	805.39	841.90	03/2013 -	12/2014	21	-
220	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	746.90	01/2014 -	12/2014	11	-
221	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	574.00	982.40	03/2014 -	12/2014	9	-
222	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	1,179.00	11/2013 -	12/2014	13	-
223	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	323.00	06/2014 -	12/2014	6	-
224	SAMBALPUR-BARGARH- CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	909.00	974.30	05/2014 -	12/2014	7	-
225	4-LANING OF BRAHMAPORE-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	998.79	1,597.00	08/2013 -	12/2014	16	-
226	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	1,047.00	294.60	06/2014 -	12/2014	6	-
227	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19 -	484.19	285.50	10/2014 -	12/2014	2	-
228	2 LANING OF DINDIGUL - PERIGULAM THENI-KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	362.20	08/2013 -	02/2015	18	-
229	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	385.13	159.20	04/2009 -	03/2015	71	-

(September 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
230	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	195.00	280.20	06/2008 -	03/2015	81	-
231	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	237.80	321.40	06/2008 -	03/2015	81	-
232	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 333.83	386.10	126.70	09/2007 -	03/2015	90	-
233	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	232.45	317.20	09/2010 -	03/2015	54	-
234	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	03/2015	40	-
235	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,415.00	06/2013 -	03/2015	21	-
236	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	535.00	52.18	12/2013 -	03/2015	15	-
237	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	406.60	04/2014 -	03/2015	11	-
238	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	825.40	07/2013 -	03/2015	20	-
239	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	835.00	475.90	01/2014 -	03/2015	14	-
240	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	500.29	632.80	08/2013 -	03/2015	19	-
241	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	356.40	250.60	07/2014 -	03/2015	8	-
242	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT	03/2012	828.00 -	828.00	763.50	09/2014 -	03/2015	6	-
243	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	2,188.00	05/2014 -	05/2015	12	-
244	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	624.00	441.40	04/2014 -	05/2015	13	-
245	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	230.00	251.50	06/2005 -	06/2015	120	-
246	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	280.13	173.80	11/2008 -	06/2015	79	-
247	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	465.50	308.10	09/2007 -	06/2015	93	-
248	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	572.30	886.90	10/2011 -	06/2015	44	-
249	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	927.40	07/2013 -	06/2015	23	-
250	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	1,078.84	1,906.00	08/2013 -	06/2015	22	-
251	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	2,786.00	08/2014 -	07/2015	11	-
252	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	398.00	461.90	02/2014 -	09/2015	19	-

(September 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
253	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	787.90	09/2014 -	10/2015	13	-
254	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	2,388.00	2,249.00	06/2014 -	11/2015	17	-
255	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	682.00	729.40	10/2013 -	11/2015	25	-
256	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	495.40	12/2009 -	12/2015	72	-
257	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	325.00	609.50	05/2013 -	12/2015	31	-
258	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,134.00	03/2014 -	12/2015	21	-
259	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	209.00	38.77	01/2013 -	12/2015	35	-
260	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	398.50	09/2013 -	12/2015	27	-
261	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	591.50	03/2013 -	12/2015	33	-
262	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	580.43	430.20	08/2013 -	12/2015	28	-
263	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	141.10	01/2014 -	12/2015	23	-
264	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	719.20	07/2014 -	12/2015	17	-
265	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	478.00	321.20	10/2013 -	12/2015	26	-
266	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	942.69	286.60	06/2014 -	12/2015	18	-
267	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	867.00	598.60	02/2015 -	02/2016	12	-
268	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	156.60	08/2012 -	03/2016	43	-
269	NASHRI CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	06/2010	2,159.00 -	2,159.00	622.70	06/2015 -	05/2016	11	-
270	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,170.00	07/2015 -	06/2016	11	-
271	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	281.31	181.10	02/2010 -	07/2016	77	-
272	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	39.55	09/2013 -	12/2016	39	-
273	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2016	35	-
	Total		65,879.03 -	67,854.08	65,626.41				
	<u>SHIPPING AND PORTS</u>								
274	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 1,460.00	2,098.56	1,020.94	12/2010 09/2012	03/2015	51	30

(September 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	Total		1,228.00 -	2,098.56	1,020.94				
	<u>TELECOMMUNICATIONS</u>								
275	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTARANCHAL - [N26000058]BSNL,UTTARAKHAND	01/2009	149.15 -	158.72	86.05	06/2009 -	12/2014	66	-
276	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL,ASSAM	06/2007	336.81 -	336.81	195.94	01/2009 -	12/2014	71	-
	Total		485.96 -	495.53	281.99				
	<u>URBAN DEVELOPMENT</u>								
277	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA - [N28000078]CPWD,BIHAR	11/2006	2,727.89 -	2,727.89	2,637.11	03/2010 -	10/2014	55	-
278	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	205.00	93.74	03/2012 -	01/2015	34	-
279	FARIDABAD EXTENSION - [N28000057]DMRC,DELHI	09/2011	2,494.00 -	2,494.00	685.21	09/2014 -	05/2015	8	-
280	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD,WEST BENGAL	01/2009	225.81 -	225.81	17.60	06/2012 -	05/2015	35	-
281	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD,ODISHA	11/2012	238.43 -	238.43	-	02/2015 -	08/2015	6	-
282	C/O NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 -	315.00	53.96	06/2015 -	08/2015	2	-
283	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	15.60	11/2014 -	10/2015	11	-
284	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85 -	261.85	101.52	05/2013 -	10/2015	29	-
285	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	884.30	103.45	08/2014 -	01/2016	17	-
286	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI	05/2012	405.01 -	405.01	-	12/2014 -	04/2016	16	-
287	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	-	03/2016 -	05/2016	2	-
288	CONSTRUCTION OF CENTRAL ACADEMY FOR PUBLIC TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	188.87	10.64	12/2014 -	12/2016	24	-
289	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	-	09/2015 -	12/2016	15	-

(September 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	Total		8,545.42	8,545.42	3,718.83				
	Grand Total		526,114.10	610,116.12	379,650.65				
