

**407th FLASH REPORT ON
CENTRAL SECTOR PROJECTS
(Rs.150 crore and above)
September, 2019**



KUDANKULAM NUCLEAR POWER PROJECT UNIT-3



सत्यमेव जयते

Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division

Khurshid Lal Bhawan, Janpath
New Delhi-110001
Website: www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India Ltd.
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead Travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised Catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Operation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petroleum Corporation Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative Ltd.
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation Ltd.
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Corporation.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Corporation.
NCL	Northern Coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation Ltd.
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corporation Ltd.
NGN	Next Generation Network
NLC	Neyveli Lignite Corporation Ltd.
NMDC	National Mineral Development Corporation Ltd.
NPC	Nuclear Power Corporation Ltd.
NRL	Numaligarh Refinery Ltd.
OB	Over Burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over Bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India Ltd.
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

EXECUTIVE SUMMARY

1. The Flash Report for September 2019 contains information on the status of the 1635 Central Sector Infrastructure Projects costing ₹150 crore and above. During September 2019, 2 projects (Petroleum Sector) have reported completion.

2. During the reference month, out of 1635 projects, 565 projects are delayed with respect to their original schedules and 59 projects have reported additional delays vis-à-vis their date of completion reported in the previous month. Of these 59 projects, 22 are Mega Projects costing ₹1000 crore and above.

S.No.	Sector	Projects on monitor (No.)	Delayed Projects w.r.t original schedule (No.)	Additionally delayed during the month under report (No.)	Additionally delayed Mega Projects (No.)
1	ROAD TRANSPORT AND HIGHWAYS	856	225	21	5
2	RAILWAYS	315	146	12	8
3	PETROLEUM	150	52	7	3
4	COAL	107	37	2	1
5	POWER	76	49	13	4
6	URBAN DEVELOPMENT	63	24	2	0
7	HEALTH AND FAMILY WELFARE	21	10	0	0
8	CIVIL AVIATION	13	5	0	0
9	STEEL	9	8	1	1
10	FERTILISERS	5	1	0	0
11	MINES	5	0	0	0
12	ATOMIC ENERGY	4	4	0	0
13	TELECOMMUNICATIONS	4	2	1	0
14	INFORMATION AND BROADCASTING	3	1	0	0
15	WATER RESOURCES	2	1	0	0
16	HEAVY INDUSTRY	1	0	0	0
17	SHIPPING AND PORTS	1	0	0	0
Total		1635	565	59	22

3. Total original cost of implementation of the 1635 projects was ₹19,47,462.67 crore and their anticipated completion cost is likely to be ₹23,41,784.84 crore, which reflects overall cost overruns of ₹3,94,322.17 crore (20.25% of original cost). The expenditure incurred on these projects till September 2019 is ₹9,96,613.94 crore, which is 42.55% of the anticipated cost of the projects. The

sector-wise list of projects (maximum five in numbers) having maximum percentage of cost overruns is as follows:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Percentage of Cost Overruns (as on 01-10-2019)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (%)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6840.00	95.88
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	16580.00	44.69
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	10/2009	12320.00	17079.00	38.63
CIVIL AVIATION					
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	314.61	441.33	40.28
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	859.86	860.00	0.02
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	09/2015	338.93	339.00	0.02
COAL					
7	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.49	201.44
8	BHANEAGAON OC	02/2015	187.94	409.68	117.98
9	RCE OF INDARAM OCP(1.20 MTPA)	07/2011	162.76	349.28	114.60
10	RANIGANJ MASTER PLAN	08/2009	2661.73	5186.24	94.84
11	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	249.03	448.86	80.24
FERTILISERS					
12	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	209.44	5.89
HEALTH AND FAMILY WELFARE					
13	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	513.89	24.10
14	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	523.00	3.45
15	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	156.56	156.65	0.06
PETROLEUM					
16	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	1683.06	95.30
17	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	70.49
18	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	06/2010	202.94	345.92	70.45
19	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	01/2015	1823.00	3027.90	66.09
20	HALDIA LPG IMPORT FACILITY	03/2015	694.00	1097.54	58.15
POWER					
21	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	7927.34	217.49
22	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19496.34	210.19
23	TEHRI PUMPED STORAGE PLANT(1000MW)	07/2006	1657.00	5024.35	203.22
24	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	9997.11	155.05
25	BARH STPP(3X660MW) NTPC	02/2005	8692.97	21312.11	145.16
RAILWAYS					
26	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	6093.31	2360.35

27	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI	04/2011	120.70	1800.00	1391.30
28	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	27949.00	1017.96
29	BIHTA-AURANGABAD (NL)	04/2008	326.20	2995.01	818.15
30	ATTIPPATTU PUTTUR	04/2008	151.84	1105.00	627.74
ROAD TRANSPORT AND HIGHWAYS					
31	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I) NEW	09/2015	771.18	7558.00	880.06
32	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	655.17	234.27
33	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2967.50	167.82
34	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	167.64	408.77	143.84
35	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	08/2010	195.04	377.99	93.80
SHIPPING AND PORTS					
36	JAL MARG VIKAS PROJECT	01/2018	4200.00	5369.18	27.84
STEEL					
37	NMDC INTEGRATED STEEL PLANT	01/2010	15525.00	23140.00	49.05
TELECOMMUNICATIONS					
38	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	84.97
39	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	01/2018	231.80	240.10	3.58
URBAN DEVELOPMENT					
40	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	114.26	266.00	132.80
41	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	2000.00	64.04
42	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1113.34	44.80
43	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	19058.00	30.53
44	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	02/2014	388.00	488.28	25.85
WATER RESOURCES					
45	POLAVARAM IRRIGATION PROJECT	02/2009	10151.04	55548.87	447.22

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overrun.

4. The sector wise list of projects (maximum five in numbers) having maximum cost overruns (COR) in absolute term is as below:-

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Cost Overruns (COR)
(as on 01-10-2019)**

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (Rs.crore)
ATOMIC ENERGY					
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	16580.00	5121.00
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12320.00	17079.00	4759.00
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6840.00	3348.00
CIVIL AVIATION					

4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	314.61	441.33	126.72
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	859.86	860.00	0.14
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	09/2015	338.93	339.00	0.07
COAL					
7	RANIGANJ MASTER PLAN	08/2009	2661.73	5186.24	2524.51
8	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	06/2011	5907.11	7080.41	1173.30
9	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.49	307.06
10	BHANEAGAON OC	02/2015	187.94	409.68	221.74
11	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	249.03	448.86	199.83
FERTILISERS					
12	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	209.44	11.65
HEALTH AND FAMILY WELFARE					
13	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	513.89	99.78
14	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	523.00	17.42
15	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	156.56	156.65	0.09
PETROLEUM					
16	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	05/2016	4497.00	6025.00	1528.00
17	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	01/2015	1823.00	3027.90	1204.90
18	PARADIP HYDERABAD PIPELINE	01/2015	2321.00	3338.00	1017.00
19	MUMBAI REFINERY EXPANSION PROJECT	09/2015	4199.00	5060.00	861.00
20	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	1683.06	821.27
POWER					
21	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19496.34	13211.01
22	BARH STPP(3X660MW) NTPC	02/2005	8692.97	21312.11	12619.14
23	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	9997.11	6077.52
24	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	7927.34	5430.44
25	BRBCL-NABINAGAR TPP- JV (4X250 MW)	01/2007	5353.00	9996.59	4643.59
RAILWAYS					
26	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	16592.00	51101.00	34509.00
27	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	27949.00	25449.00
28	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	11589.00	28181.00	16592.00
29	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	4454.17	12524.00	8069.83
30	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	6093.31	5845.65
ROAD TRANSPORT AND HIGHWAYS					
31	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I) NEW	09/2015	771.18	7558.00	6786.82
32	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2967.50	1859.50
33	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	03/2016	1587.49	2982.00	1394.51
34	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	08/2016	1388.34	2525.80	1137.46
35	DELHI AGRA APPROVED LENGTH 180.0 KM	10/2012	1928.22	2945.00	1016.78
SHIPPING AND PORTS					
36	JAL MARG VIKAS PROJECT	01/2018	4200.00	5369.18	1169.18
STEEL					
37	NMDC INTEGRATED STEEL PLANT	01/2010	15525.00	23140.00	7615.00
TELECOMMUNICATIONS					
38	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	11330.00
39	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	01/2018	231.80	240.10	8.30
URBAN DEVELOPMENT					

40	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	19058.00	4458.00
41	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	2000.00	780.79
42	KOCHI METRO RAIL PROJECT	07/2012	5181.79	5687.79	506.00
43	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1113.34	344.46
44	REDEVELOPMENT OF EAST KIDWAI NAGAR	06/2012	4264.00	4439.23	175.23
WATER RESOURCES					
45	POLAVARAM IRRIGATION PROJECT	02/2009	10151.04	55548.87	45397.83

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overruns.

5. Out of the 1635 projects, 353 are on schedule, 565 are delayed, 377 projects reported cost overrun and 187 projects reported both time and cost overrun with respect to their original project implementation schedules. However, the number of delayed projects decreases to 495 if delay is calculated on the basis of latest schedule of completion. Further, for 693 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 565 delayed projects, 182 (32.21%) projects have overall delay in the range of 1 to 12 months, 129 (22.83%) projects have delay in the range of 13 to 24 months, 140 (24.78%) projects have delay in the range of 25 to 60 months and 114 (20.18%) projects have delay of 61 months and above. **The average time overrun in these 565 delayed projects is 38.41 months.** The sector wise list of projects (maximum five in numbers) having maximum time overruns (TOR) are as below:

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Time Overruns (TOR)
(as on 01-10-2019)

SN	PROJECT	DOA	DOC ORIGINAL	DOC ANTICIPATED	TOR (IN MONTHS)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	09/2010	10/2021	133
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	06/2020	54
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	10/2009	12/2016	12/2020	48
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	03/2013	11/2020	11/2023	36
CIVIL AVIATION					
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	09/2018	06/2020	21
6	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA	01/2016	03/2020	12/2020	9
7	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	11/2016	04/2020	12/2020	8
8	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	09/2015	06/2019	12/2019	6
9	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	06/2018	02/2022	08/2022	6
COAL					
10	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	03/2010	03/2022	144

11	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	03/2012	03/2024	144
12	RAMAGUNDAM OC-II EXTENSION	12/2009	03/2012	03/2023	132
13	KULDA OCP (MAHANADI COALFIELDS LTD)	01/2005	03/2010	03/2020	120
14	CHURI BENTI UG (0.81 MTY)	08/2007	03/2011	03/2021	120
	FERTILISERS				
15	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	11/2016	09/2019	34
	HEALTH AND FAMILY WELFARE				
16	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	11/2013	10/2020	83
17	AIIMS - MOTHER AND CHILD BLOCK	12/2013	05/2017	09/2019	28
18	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	07/2016	02/2018	09/2019	19
19	NEIGRIHMS SHILLONG MEGHALYA	10/2016	05/2018	09/2019	16
20	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	08/2017	03/2019	03/2020	12
	INFORMATION AND BROADCASTING				
21	FILM AND TELEVISION INSTITUTE ARUNACHAL PRADESH	11/2016	02/2019	11/2019	9
	PETROLEUM				
22	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	12/2012	02/2022	110
23	ASSAM RENEWAL PROJECT FOR GROUP A	03/2009	03/2013	12/2019	81
24	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	05/2013	12/2019	79
25	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	06/2010	01/2014	11/2019	70
26	INTEGRATED DEVELOPMENT OF B-127 FIELDS	12/2011	03/2015	12/2019	57
	POWER				
27	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	09/2009	12/2021	147
28	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009	10/2019	118
29	BARH STPP(3X660MW) NTPC	02/2005	10/2011	08/2021	118
30	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	08/2008	06/2013	12/2022	114
31	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	02/2009	08/2013	03/2022	103
	RAILWAYS				
32	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	04/1998	03/2003	03/2030	324
33	BANGLORE - SATYAMANGALAM (NL)(SWR)	04/1996	03/2002	03/2024	264
34	MUNEERABAD-MAHABOBNAGAR(NL),SCR	04/1997	03/2000	03/2021	252
35	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL	04/2010	03/2005	03/2025	240
36	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	11/2002	06/2022	235
	ROAD TRANSPORT AND HIGHWAYS				
37	SONAPUR TO GUWAHTI (AS-3)	12/2003	03/2008	08/2020	149
38	NALBARI T BIJNI (AS-7)	12/2003	04/2008	03/2020	143
39	NALBARI TO BIJNI (AS-6)	12/2003	06/2008	10/2019	136
40	GWALIOR-JHANSI, NH-75	12/2003	12/2009	08/2020	128
41	DELHI/ HARYANA BORDER TO ROHTAK	04/2007	05/2010	03/2020	118
	STEEL				
42	NMDC INTEGRATED STEEL PLANT	01/2010	05/2015	07/2020	62
43	NEW SINTER PLANT AT BOKARO STEEL PLANT	03/2015	10/2017	06/2020	32
44	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	05/2015	12/2017	11/2019	23
45	COKE OVEN BATTERY-5	12/2011	12/2017	10/2019	22
46	INSTALLATION OF NEW HOT STRIP MILL	04/2015	04/2018	11/2019	19

	AT RSP				
	TELECOMMUNICATIONS				
47	NETWORK FOR SPECTRUM	03/2012	07/2015	05/2020	58
48	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	01/2018	10/2018	12/2019	14
	URBAN DEVELOPMENT				
49	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	10/2012	03/2020	89
50	IRRIGATION WORK OF BAGMATI	10/2005	03/2015	03/2021	72
51	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	12/2013	10/2019	70
52	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	02/2014	03/2015	10/2020	67
53	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	01/2015	05/2020	64
	WATER RESOURCES				
54	POLAVARAM IRRIGATION PROJECT	02/2009	03/2020	06/2021	15

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further time overruns.

6. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in forest clearance, delay in supply of equipments, fund constraints, geological surprises, problems in equipment erection, geo-mining conditions, slow progress in civil works, shortage of labour, inadequate mobilization by the contractor, maoist problems, court cases, contractual issues, ROU/ROW problems, law and order situation etc.

7. The Online Computerized Monitoring System (OCMS) of this Ministry envisages monitoring of milestones of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The sector wise list of earliest projects (maximum five in numbers) without milestones are as below:-

**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Milestones
(as on 01-10-2019)**

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST ANTICIPATED (Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)	ORIGINAL DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
	CIVIL AVIATION						
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	314.61	441.33	85.79	09/2018	06/2020
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	09/2015	338.93	339.00	213.50	06/2019	12/2019
3	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA	01/2016	219.91	219.91	61.61	03/2020	12/2020

4	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	11/2016	233.38	233.38	84.73	04/2020	12/2020
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	859.86	860.00	232.44	03/2021	03/2021
COAL							
6	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	03/2015	513.63	513.63	175.30	12/2019	N.A.
7	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	03/2015	522.45	522.45	9.88	09/2019	N.A.
8	COAL PROJECT NAME JAMUNIA UG (0.84 MTY)	07/2016	409.87	409.87	20.30	03/2022	03/2022
9	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	07/2016	17237.00	17237.80	7532.67	11/2021	11/2021
10	KOLAR PIMPRI EXTENSION OC	03/2017	362.73	362.73	319.93	03/2020	03/2020
HEALTH AND FAMILY WELFARE							
11	LGBRIMH-TEZPUR, ASSAM	07/2012	175.57	175.57	113.50	12/2014	N.A.
12	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	513.89	147.00	11/2013	10/2020
13	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	07/2016	703.00	703.00	184.93	06/2020	08/2020
14	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	07/2016	785.00	785.00	244.66	04/2020	06/2020
15	CNCI KOLKATA WEST BENGAL	08/2016	244.00	244.00	241.39	09/2018	N.A.
HEAVY INDUSTRY							
16	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	08/2016	1554.00	1554.00	335.03	09/2019	09/2019
INFORMATION AND BROADCASTING							
17	NATIONAL FILM HERITAGE MISSION	11/2014	597.41	597.41	29.80	N.A.	N.A.
18	FILM AND TELEVISION INSTITUTE ARUNACHAL PRADESH	11/2016	204.32	204.32	0.00	02/2019	11/2019
19	NATIONAL CENTRE OF EXCELLENCE FOR ANIMATION VISUAL EFFECTS GAMING AND COMICS	12/2016	167.70	167.70	0.00	03/2020	03/2020
PETROLEUM							
20	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	1549.85	01/2012	N.A.
21	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	07/2011	350.00	350.00	2.06	01/2019	09/2019
22	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	678.00	678.00	5.57	02/2017	10/2021
23	ENNORE-TRICHY-MADURAI LPG PIPELINE	05/2013	711.00	711.00	11.12	06/2020	06/2020
24	REVAMPING OF MARKETING TERMINAL AT	07/2014	247.00	247.00	0.00	03/2021	03/2021

	VISHAKHAPATNAM						
	POWER						
25	LOKTAK D/S HEP(NHPC)	12/1999	578.62	578.62	0.00	06/2006	N.A.
26	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19496.34	10989.45	09/2010	N.A.
27	PAKRI BARWADIH COAL MINING PROJECT	10/2004	4237.96	4552.00	3268.00	10/2017	N.A.
28	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	01/2014	374.63	374.63	213.02	04/2016	12/2019
29	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	4754.42	9072.36	1301.58	12/2018	12/2020
	RAILWAYS						
30	HOWRAH-AMTA- CHAMPADANGA NL (SER)	04/1974	393.46	1026.00	182.49	03/2007	N.A.
31	NANGALDAM- TALWARA(NL),NR	03/1981	450.00	2010.00	654.07	07/2012	03/2024
32	NEW BG RLY LINE FROM EKLAKHI- BALURGHAT INCLUDING GAZOLE- ITAHAR(NL),NEFR	04/1983	297.32	614.00	274.97	03/2019	03/2020
33	LAKSHMIKANTAPUR- NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA- CHANDRANAGAR, KAKDWIP- BUDAKHALI AND CHANDRANAG	04/1987	406.99	545.70	148.43	03/2006	03/2025
34	MUZAFFARPUR- SITAMARHI NEW LINE	01/1991	332.15	546.71	541.07	07/2014	N.A.
	ROAD TRANSPORT AND HIGHWAYS						
35	FOUR LANING OF BHOJPUR TO BUXAR	01/1991	642.41	642.41	131.71	N.A.	10/2020
36	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	01/1991	478.35	478.35	0.00	N.A.	N.A.
37	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	01/1991	319.68	369.77	113.67	N.A.	N.A.
38	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	01/1991	219.40	219.40	0.00	01/2018	N.A.
39	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	282.41	322.01	278.45	08/2016	N.A.
	SHIPPING AND PORTS						
40	JAL MARG VIKAS PROJECT	01/2018	4200.00	5369.18	1400.95	03/2023	03/2023
	TELECOMMUNICATIONS						
41	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	8397.00	07/2015	05/2020

42	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	06/2016	418.26	418.26	367.03	06/2017	N.A.
43	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	01/2018	231.80	240.10	117.63	10/2018	12/2019
URBAN DEVELOPMENT							
44	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1113.34	1085.64	02/2014	N.A.
45	IRRIGATION WORK OF BAGMATI	10/2005	956.00	956.00	651.21	03/2015	03/2021
46	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	175.94	178.65	12/2015	N.A.
47	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	08/2007	246.90	246.90	0.00	N.A.	N.A.
48	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	202.61	227.00	199.95	12/2016	N.A.
WATER RESOURCES							
49	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA	03/2017	233.57	233.57	32.20	12/2019	12/2019

N.A.: Not Available.

N.B.: The concerned administrative Ministry may like review these Projects in order to firm-up milestones.

9. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The sector wise list of earliest (oldest) projects (maximum five in numbers) without revised cost estimates are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Cost Estimates (as on 01-10-2019)

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST REVISED(Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	0.00	5821.38
COAL					
2	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	249.03	0.00	286.19
3	BHUBANESWARI OCP, MCL (20.0 MTY)	12/2007	490.10	0.00	501.82
4	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	172.08	0.00	347.15
5	KANIHA OCP, MCL, (10.0 MTY)	12/2007	457.77	0.00	539.59

6	ANANTA OC EXPANSION PH-III (15.0 MTY)	08/2008	207.28	0.00	228.90
	HEALTH AND FAMILY WELFARE				
7	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	0.00	508.29
	PETROLEUM				
8	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	0.00	1549.85
9	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	0.00	1322.31
	POWER				
10	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	0.00	7642.51
11	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	0.00	10989.45
12	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	05/2005	1779.29	0.00	2237.45
13	TEHRI PUMPED STORAGE PLANT(1000MW)	07/2006	1657.00	0.00	3047.08
14	BRBCL-NABINAGAR TPP- JV (4X250 MW)	01/2007	5353.00	0.00	7918.78
	RAILWAYS				
15	NANGALDAM-TALWARA(NL),NR	03/1981	450.00	0.00	654.07
16	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	04/1991	329.39	803.11	1029.84
17	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	09/1995	303.98	0.00	669.21
18	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	02/1996	268.87	0.00	927.86
19	NANDYAL-YERRAGUNTALA(NL),SCR	03/1996	164.36	0.00	999.64
	ROAD TRANSPORT AND HIGHWAYS				
20	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	280.00	456.92	488.37
21	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	160.00	0.00	223.81
22	NALBARI T BIJNI (AS-7)	12/2003	208.00	0.00	337.76
23	NALBARI TO BIJNI (AS-6)	12/2003	225.00	0.00	328.47
24	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	217.61	0.00	451.15
	STEEL				
25	NMDC INTEGRATED STEEL PLANT	01/2010	15525.00	0.00	16064.29
	URBAN DEVELOPMENT				
26	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1070.97	1085.64
27	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	173.00	178.65
28	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	0.00	16352.87
29	KOCHI METRO RAIL PROJECT	07/2012	5181.79	0.00	5188.00
30	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	02/2014	388.00	0.00	437.01
	WATER RESOURCES				
31	POLAVARAM IRRIGATION PROJECT	02/2009	10151.04	0.00	16417.99

N.B.: The concerned administrative Ministry may like to review these Projects in order to firm-up revised cost estimates.

10. The sector wise list of earliest projects (maximum five in numbers) without revised commissioning schedule are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Commissioning Schedule (as on 01-10-2019)

SN	SECTOR/ PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	REVISED DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
COAL					
1	KAKATIYA LONGWALL	12/2008	12/2012	N.A.	N.A.
2	RANIGANJ MASTER PLAN	08/2009	08/2019	N.A.	N.A.
3	MANUGURU OC-II EXTENSION PHASE-II	03/2010	03/2012	N.A.	N.A.
4	MURADIH UG TURN-KEY PROJECT	02/2011	04/2014	N.A.	N.A.
5	MOONIDH XV SEAM UG	08/2011	04/2015	N.A.	N.A.
HEALTH AND FAMILY WELFARE					
6	LGBRIMH-TEZPUR, ASSAM	07/2012	12/2014	N.A.	N.A.
7	AIIMS - MOTHER AND CHILD BLOCK	12/2013	05/2017	N.A.	N.A.
8	AIIMS - OPD(NEW)	08/2014	05/2017	N.A.	N.A.
9	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	03/2018	N.A.	N.A.
10	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	07/2016	02/2018	N.A.	N.A.
INFORMATION AND BROADCASTING					
11	NATIONAL FILM HERITAGE MISSION	11/2014	N.A.	N.A.	N.A.
MINES					
12	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU	09/2017	06/2019	N.A.	N.A.
PETROLEUM					
13	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	01/2012	N.A.	N.A.
14	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II	11/2011	03/2013	N.A.	N.A.
15	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	09/2012	03/2015	N.A.	N.A.
16	RESID UPGRADATION PROJECT	03/2013	11/2015	N.A.	N.A.
17	POLYPROPYLENE PLANT AT PARADIP REFINERY	03/2014	09/2017	N.A.	N.A.
POWER					
18	LOKTAK D/S HEP(NHPC)	12/1999	06/2006	N.A.	N.A.
19	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	09/2010	N.A.	N.A.
20	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017	N.A.	N.A.
21	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	05/2005	11/2008	N.A.	N.A.
22	MOUDA STPP STAGE 2	03/2012	09/2016	N.A.	N.A.
RAILWAYS					
23	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	03/2007	03/2007	N.A.
24	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	07/2014	N.A.	N.A.
25	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	02/1996	03/2005	N.A.	N.A.
26	NANDYAL-YERRAGUNTLA(NL),SCR	03/1996	02/2009	N.A.	N.A.
27	ETAWAH-MAINPURI (NL),NCR	04/1997	12/2008	N.A.	N.A.
ROAD TRANSPORT AND HIGHWAYS					
28	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O	01/1991	04/2014	N.A.	N.A.
29	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	08/2016	N.A.	N.A.

30	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	10/2016	N.A.	N.A.
31	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB	01/1991	10/2017	N.A.	N.A.
32	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	01/1991	01/2018	N.A.	N.A.
TELECOMMUNICATIONS					
33	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY	09/2014	09/2014	N.A.	N.A.
34	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	06/2016	06/2017	N.A.	N.A.
URBAN DEVELOPMENT					
35	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	02/2014	N.A.	N.A.
36	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	12/2015	N.A.	N.A.
37	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	08/2007	N.A.	N.A.	N.A.
38	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND	12/2007	06/2016	N.A.	N.A.
39	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016	N.A.	N.A.

N.A.: Not Available.

N.B.: The concerned administrative Ministry may like to review these Projects in order to firm-up revised commissioning schedule.

11. The status as on 01.10.2019 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

12. This has the approval of Competent Authority, Ministry of Statistics and Programme Implementation.

TABLE-1

EXECUTIVE SUMMARY COSTING Rs.150 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	856	21
2	RAILWAYS	315	12
3	PETROLEUM	150	7
4	COAL	107	2
5	POWER	76	13
6	URBAN DEVELOPMENT	63	2
7	HEALTH AND FAMILY WELFARE	21	0
8	CIVIL AVIATION	13	0
9	STEEL	9	1
10	FERTILISERS	5	0
11	MINES	5	0
12	ATOMIC ENERGY	4	0
13	TELECOMMUNICATIONS	4	1
14	INFORMATION AND BROADCASTING	3	0
15	WATER RESOURCES	2	0
16	HEAVY INDUSTRY	1	0
17	SHIPPING AND PORTS	1	0
	Total	1635	59

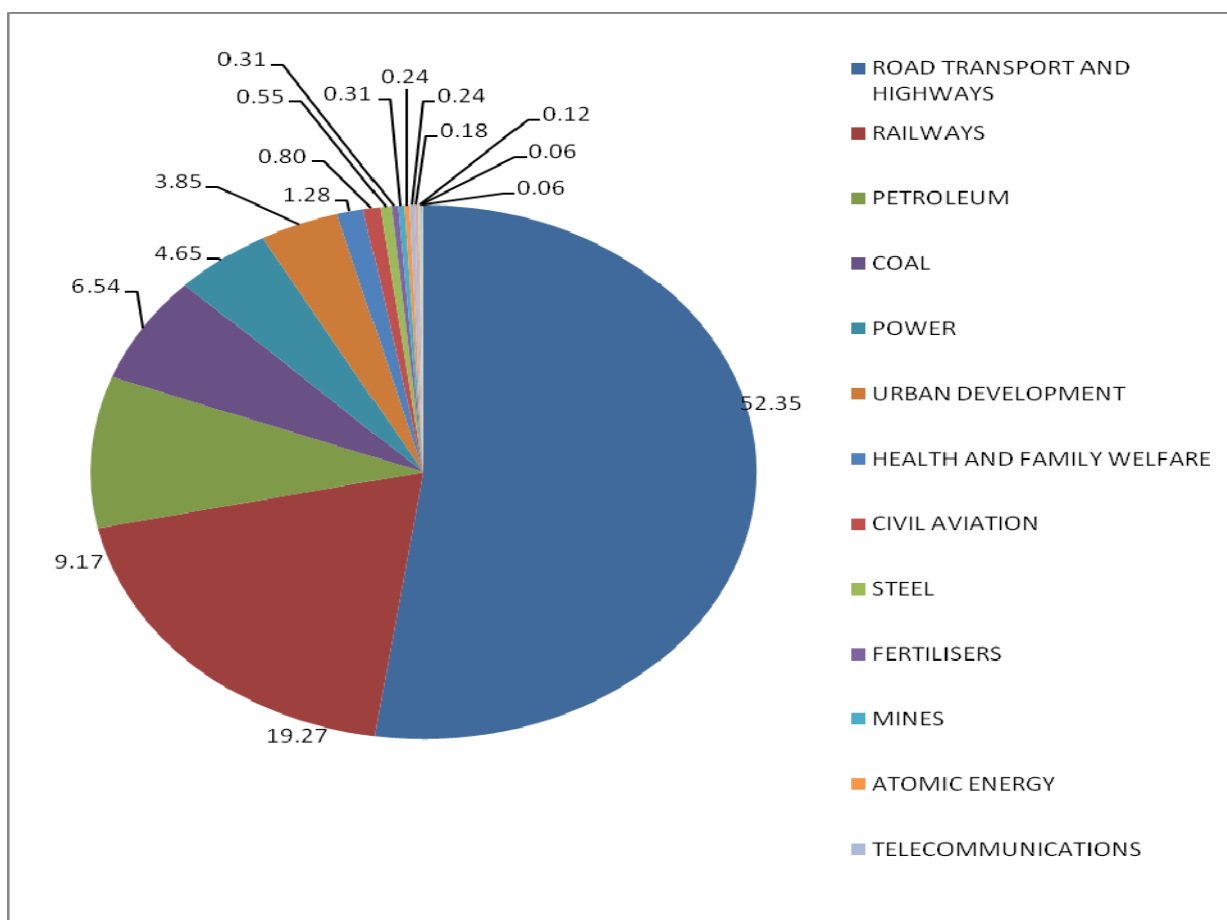


TABLE-2

Month wise List of Completed Projects Costing Rs.150 crore and above during				
2019-2020				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2019			
	<u>COAL</u>			
1	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI (NORTHERN COAL FIELDS LIMITED) - [N06000033]	259.40	03/2012	266.38
2	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) (NORTHERN COAL FIELDS LIMITED) - [N06000091]	1,131.28	03/2018	796.85
	<u>PETROLEUM</u>			
3	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000175]	3,076.00	09/2017	3,450.30
	<u>POWER</u>			
4	BONGAIGAON THERMAL POWER PROJECT (NATIONAL THERMAL POWER CORPORATION) - [N18000041]	4,375.35	10/2011	7,000.00
5	TRIPURA GAS BASED POWER PROJECT (NORTH EAST ELECTRIC POWER CORPORATION) - [N18000071]	421.01	07/2013	963.23
	<u>RAILWAYS</u>			
6	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) RAILWAY) - [N22000113]	653.19	03/2014	862.17
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
7	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000357]	567.51	03/2018	421.60
	May,2019			
	<u>COAL</u>			
8	MAKARDHOKRA I OC (WESTERN COAL FIELDS LIMITED) - [N06000119]	266.23	03/2021	144.38
	<u>PETROLEUM</u>			
9	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000084]	736.65	09/2011	331.47
10	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY Central Sector Projects(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000290]	474.15	05/2019	348.64
	<u>POWER</u>			

Month wise List of Completed Projects Costing Rs.150 crore and above during

2019-2020

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
11	WESTERN REGION STRENGTHENING SCHEME-V (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000035]	477.69	09/2010	691.96
12	KUDGI STPP STAGE 1 (NATIONAL THERMAL POWER CORPORATION) - [N18000131]	15,166.19	01/2017	15,364.00
13	SOLAPUR STPP (NATIONAL THERMAL POWER CORPORATION) - [N18000133]	9,395.18	01/2017	8,617.00
14	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000158]	539.82	06/2016	434.33
15	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000174]	3,363.12	12/2016	2,244.00
16	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000222]	790.13	06/2019	575.24
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
17	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000145]	1,585.00	05/2013	2,023.33
18	JORBAT - BARAPANI PPP (ANNUITY)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000180]	536.00	01/2014	845.41
19	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S EPC(PUBLIC WORKS DEPT OF STATE) - [N24000241]	177.18	03/2016	40.51
20	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTIO EPC(PUBLIC WORKS DEPT OF STATE) - [N24000242]	158.65	03/2016	103.50
21	YAN TO NIRMAL SEREHALITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW EPC(PUBLIC WORKS DEPT OF STATE) - [N24000243]	244.08	03/2016	38.32
22	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T EPC(PUBLIC WORKS DEPT OF STATE) - [N24000244]	340.00	03/2016	2.00
23	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO EPC(PUBLIC WORKS DEPT OF STATE) - [N24000246]	244.30	12/2016	2.00
24	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S (PUBLIC WORKS DEPT OF STATE) - [N24000249]	218.31	12/2015	208.28
25	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 (NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000250]	260.39	11/2016	188.00
26	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 EPC(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000255]	220.72	11/2016	155.30
27	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 EPC(PUBLIC WORKS DEPT OF STATE) - [N24000261]	267.16	11/2017	308.33
28	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A EPC(DEPT OF ROAD TRANSPORT & HIGHWAYS) - [N24000262]	201.12	02/2015	150.19
29	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) (PUBLIC WORKS DEPT OF STATE) - [N24000263]	241.61	02/2017	178.94

Month wise List of Completed Projects Costing Rs.150 crore and above during

2019-2020

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
30	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN EPC(PUBLIC WORKS DEPT OF STATE) - [N24000265]	297.78	02/2017	284.89
31	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC (PUBLIC WORKS DEPT OF STATE) - [N24000266]	361.30	07/2014	203.29
32	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) EPC(PUBLIC WORKS DEPT OF STATE) - [N24000267]	258.99	07/2014	200.44
33	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC EPC(PUBLIC WORKS DEPT OF STATE) - [N24000268]	251.55	02/2015	172.65
34	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T EPC(PUBLIC WORKS DEPT OF STATE) - [N24000269]	175.03	-	152.53
35	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP EPC(PUBLIC WORKS DEPT OF STATE) - [N24000272]	266.00	-	182.13
36	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000273]	314.43	-	216.96
37	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA ITEM RATE(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000277]	185.82	-	142.23
38	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500- KM 130.00 DHAMTARI- KANKER SECTION. EPC(PUBLIC WORKS DEPT OF STATE) - [N24000278]	213.47	03/2015	182.91
39	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHAKONDA) UNDER NHDP-IV EPC(PUBLIC WORKS DEPT OF STATE) - [N24000279]	298.34	03/2015	269.93
40	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHAKONDA TO JAGDALPUR) UNDER NHDP-I EPC(PUBLIC WORKS DEPT OF STATE) - [N24000280]	262.54	03/2015	215.11
41	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00- 342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- ITEM RATE(PUBLIC WORKS DEPT OF STATE) - [N24000283]	169.26	12/2012	280.72
42	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO EPC(PUBLIC WORKS DEPT OF STATE) - [N24000284]	170.21	11/2014	140.09
43	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849- KM 317.406 KAWARDHA- SIMGA SECTION. EPC(PUBLIC WORKS DEPT OF STATE) - [N24000286]	394.20	-	332.62
44	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000288]	422.34	-	406.40
45	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE EPC(PUBLIC WORKS DEPT OF STATE) - [N24000289]	435.90	-	380.41
46	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 EPC(PUBLIC WORKS DEPT OF STATE) - [N24000290]	279.68	-	286.96
47	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO EPC(PUBLIC WORKS DEPT OF STATE) - [N24000291]	463.65	-	536.84

Month wise List of Completed Projects Costing Rs.150 crore and above during

2019-2020

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
48	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM EPC(PUBLIC WORKS DEPT OF STATE) - [N24000292]	573.96	-	557.08
49	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000293]	480.21	-	372.37
50	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 EPC(PUBLIC WORKS DEPT OF STATE) - [N24000299]	224.83	05/2015	189.85
51	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDOU EPC(PUBLIC WORKS DEPT OF STATE) - [N24000300]	309.01	09/2015	391.89
52	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION EPC(PUBLIC WORKS DEPT OF STATE) - [N24000303]	417.61	06/2014	261.29
53	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 EPC(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000310]	377.83	07/2017	318.66
54	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO EPC(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000329]	497.89	04/2017	735.92
55	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000330]	629.74	-	721.04
56	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000336]	227.74	10/2016	187.85
57	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000369]	269.26	10/2016	212.72
58	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI EPC(PUBLIC WORKS DEPT OF STATE) - [N24000370]	483.38	-	470.16
59	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 EPC(PUBLIC WORKS DEPT OF STATE) - [N24000372]	616.36	-	554.68
60	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(EPC(PUBLIC WORKS DEPT OF STATE) - [N24000374]	486.74	-	415.58
61	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 EPC(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000377]	397.04	10/2016	368.49
62	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP BOT (TOLL)(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000381]	257.80	02/2016	59.30
63	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(EPC(PUBLIC WORKS DEPT OF STATE) - [N24000383]	312.79	-	258.86
64	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOULA BYPASS(EXISTING KM.138.030 TO K EPC(PUBLIC WORKS DEPT OF STATE) - [N24000384]	319.80	-	289.40
65	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' ITEM RATE(PUBLIC WORKS DEPT OF STATE) - [N24000387]	264.16	-	533.18

Month wise List of Completed Projects Costing Rs.150 crore and above during

2019-2020

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
66	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA ITEM RATE(PUBLIC WORKS DEPT OF STATE) - [N24000390]	1,494.48	02/2011	2,158.50
67	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH EPC(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000393]	774.57	03/2018	613.58
68	SHAHNOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 EPC(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000394]	532.49	05/2017	386.02
69	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 EPC(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000399]	317.76	03/2017	344.30
70	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 EPC(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000403]	283.45	10/2016	285.18
71	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM EPC(PUBLIC WORKS DEPT OF STATE) - [N24000404]	578.38	-	481.30
72	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA EPC(PUBLIC WORKS DEPT OF STATE) - [N24000405]	789.83	-	608.55
73	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAUJI ITEM RATE(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000406]	208.87	05/2016	206.78
74	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM ITEM RATE(PUBLIC WORKS DEPT OF STATE) - [N24000409]	176.22	02/2018	0.10
75	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A EPC(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000410]	641.02	12/2017	449.66
76	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 EPC(PUBLIC WORKS DEPT OF STATE) - [N24000416]	224.83	04/2015	189.85
77	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 EPC(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000418]	493.94	03/2017	503.25
78	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA ITEM RATE(PUBLIC WORKS DEPT OF STATE) - [N24000419]	165.00	09/2010	174.57
79	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF ITEM RATE(PUBLIC WORKS DEPT OF STATE) - [N24000420]	104.00	09/2010	218.29
80	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 EPC(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000421]	235.08	05/2018	235.08
81	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP BOT (TOLL)(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000447]	670.82	02/2015	590.00
82	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A (NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000474]	327.32	05/2017	301.41
83	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000476]	273.06	-	199.72

Month wise List of Completed Projects Costing Rs.150 crore and above during

2019-2020

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
84	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000512]	207.88	-	179.58
85	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO EPC(PUBLIC WORKS DEPT OF STATE) - [N24000526]	899.21	-	748.74
86	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000529]	207.88	-	179.58
87	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000536]	377.64	03/2014	755.28
88	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO (PUBLIC WORKS DEPT OF STATE) - [N24000538]	292.98	11/2014	160.96
89	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR- HYDERABAD SECTION NS-60 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000561]	244.00	07/2018	231.90
90	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000573]	322.01	08/2014	267.00
91	FUNDED)2 LANING FROM CHANGLANG DISTRICT BOUNDARY - KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000615]	334.22	06/2016	334.22
92	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000647]	162.51	05/2016	136.31
93	WIDENING TO 2 LANE WITH PAVED SHOULDER AND STRENGTHENING FROM KM 88 TO 130 ON NH-86 (PUBLIC WORKS DEPT OF STATE) - [N24000856]	170.00	02/2015	115.57
94	REHABILITATION AND UPGRADATION OF PURANPUR - KHUTAR SECTION FROM KM 38.00 TO KM 82.00 OF NH-730 TO 2 (PUBLIC WORKS DEPT OF STATE) - [N24001142]	225.96	06/2018	174.63
	June,2019			
	<u>RAILWAYS</u>			
95	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) (NORTH CENTRAL RAILWAY) - [220100007]	158.77	03/1994	682.34
96	AMRAVATI-NARKHER NL(CR) (CENTRAL RAILWAYS) - [220100118]	663.01	06/1999	726.33
97	CALICUT-MANGALORE (DL) (SR) (SOUTHERN RAILWAY) - [220100151]	240.00	-	0.01
98	MANDARHILL-DUMKA-RAMPURHAT (NL),ER (EASTERN RAILWAYS) - [220100168]	1,125.89	03/2016	1,180.08
99	KARUR-SALEM(NL),SR (SOUTHERN RAILWAY) - [220100191]	155.55	-	863.54
100	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR (NORTH CENTRAL RAILWAY) - [220100243]	108.00	12/2009	455.39
101	KATIHAR - JOGBANI (GC)(NEFR) (NORTH EAST FRONTIER RAILWAY) - [220100247]	792.46	12/2010	944.80

Month wise List of Completed Projects Costing Rs.150 crore and above during

2019-2020

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
102	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) (NORTH EASTERN RAILWAY) - [220100256]	744.71	-	917.49
103	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) (SOUTHERN RAILWAY) - [220100263]	280.00	-	942.28
104	JIND-SONEPAT (NL),NR (NORTHERN RAILWAY) - [220100280]	238.56	03/2012	785.75
105	KODERMA GIRIDH (NL), ECR (EAST CENTRAL RAILWAYS) - [220100306]	768.87	-	988.38
106	MAHARAJGANJ-MASRAKH (NL) - NER (NORTH EASTERN RAILWAY) - [220100316]	218.19	06/2018	380.50
107	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) (RAIL VIKAS NIGAM LTD.) - [N22000049]	732.81	03/2008	2,191.46
108	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE (SOUTHERN RAILWAY) - [N22000080]	343.17	-	1,110.44
109	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) (NORTHERN RAILWAY) - [N22000088]	369.90	03/2010	891.24
110	AGARTALA SABROOM, NL, NEFR (NORTH EAST FRONTIER RAILWAY) - [N22000099]	1,142.00	03/2014	3,354.18
111	DAKSHIN-BARASAL-LAKSHMIKANTAPUR (EASTERN RAILWAYS) - [N22000116]	259.51	02/2012	148.37
112	GHUTIASHARIF-CANNING (ER) (EASTERN RAILWAYS) - [N22000117]	193.08	12/2011	154.30
113	PANDABESWAR-CHINPAI DOUBLING (ER) (EASTERN RAILWAYS) - [N22000118]	293.74	12/2010	128.78
114	BHOJIPUR TANAKPUR VIA PILIBHIT (NORTH EASTERN RAILWAY) - [N22000132]	195.64	-	450.62
115	AUNRIHAR MANDUADIH (NORTH EASTERN RAILWAY) - [N22000133]	199.75	08/2018	287.33
116	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING (SOUTH EASTERN RAILWAY) - [N22000164]	309.44	12/2015	529.27
117	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC (SOUTHERN RAILWAY) - [N22000188]	271.24	-	468.58
118	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA (NORTH EAST FRONTIER RAILWAY) - [N22000194]	895.00	03/2007	1,566.57
119	CHENGANNUR-CHINGAVANAM (SOUTHERN RAILWAY) - [N22000203]	191.72	-	447.03
120	LUMDING-HOJAI PATCH DOUBLING PROJECT (NORTH EAST FRONTIER RAILWAY) - [N22000211]	246.07	03/2019	490.29
121	MEERUT-MUZAFARNAGAR PATCH DL (NORTHERN RAILWAY) - [N22000267]	377.44	-	430.12
122	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER- CHANDIGARH (NORTHERN RAILWAY) - [N22000290]	338.54	-	384.61
123	JAKHAL-MANSA DOUBLING ON SPR SECTION (NORTHERN RAILWAY) - [N22000291]	162.96	-	160.25
124	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI (SOUTHERN RAILWAY) - [N22000303]	460.94	01/1999	0.01
125	MADURAI - RAMESWARAM (161 KM) GAUGE CONVERSION (SOUTHERN RAILWAY) - [N22000439]	458.63	03/2015	367.71
126	TRICHY - MANAMADURAI (150 KM) GAUGE CONVERSION (SOUTHERN RAILWAY) - [N22000440]	200.84	03/2014	394.51
127	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION (SOUTHERN RAILWAY) - [N22000446]	600.00	03/2010	673.80

Month wise List of Completed Projects Costing Rs.150 crore and above during

2019-2020

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
128	MADURAI-DINDIGUL (INCL. AMBADUTURAI-KODAIKANNAL ROAD) (62.05 KM) DOUBLING (SOUTHERN RAILWAY) - [N22000450]	199.55	03/2009	238.61
129	MANAMADURAI - VIRUDHUNAGAR (66.55 KM) GAUGE CONVERSION. (SOUTHERN RAILWAY) - [N22000453]	208.00	03/2012	206.20
130	MULANTURUTTI - KURUPPANTARA (24 KM) DOUBLING. (SOUTHERN RAILWAY) - [N22000454]	241.00	03/2014	293.37
131	GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR- LUCKNOW (NORTH EASTERN RAILWAY) - [N22000455]	233.00	04/1999	349.37
132	MANDHANA - BRAHMAWART NEW LINE PROJECT. (NORTH EASTERN RAILWAY) - [N22000458]	609.04	04/1999	1,806.84
133	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM (EAST CENTRAL RAILWAYS) - [N22000474]	624.47	02/2016	3,376.08
	July,2019			
	<u>COAL</u>			
134	NORTH URIMARI OCP (3.0 MTY) (CENTRAL COAL FIELDS LIMITED) - [N06000084]	179.87	03/2012	163.23
	<u>STEEL</u>			
135	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) (RASTRIYA ISPAT NIGAM LIMITED) - [N12000120]	465.85	07/2018	390.25
	<u>PETROLEUM</u>			
136	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I (GAS AUTHORITY OF INDIA LIMITED) - [N16000072]	3,957.00	12/2018	2,707.26
137	PARADIP-RAIPUR- RANCHI PIPELINE (INDIAN OIL CORPORATION LIMITED) - [N16000088]	1,793.00	12/2016	1,788.86
138	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) (INDIAN OIL CORPORATION LIMITED) - [N16000187]	191.96	05/2015	76.28
139	REPLACEMENT OF KV SECTION OF KSPL Central Sector Projects(INDIAN OIL CORPORATION LIMITED) - [N16000287]	279.00	08/2018	200.05
	<u>POWER</u>			
140	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) (SATLUJ JAL VIDYUT NIGAM LIMITED) - [N18000235]	330.00	11/2017	331.46
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
141	BHOPAL-BIORA (4L) OF NH-12 IN MP BOT (TOLL)(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [N24000380]	704.26	05/2015	5.21
	<u>TELECOMMUNICATIONS</u>			

Month wise List of Completed Projects Costing Rs.150 crore and above during

2019-2020

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
142	MADHYA PRADESH ACCESS (LOT1) Central Sector Projects(BHARAT SANCHAR NIGAM LIMITED) - [N26000110]	215.30	05/2018	33.46
	August,2019			
	<u>COAL</u>			
143	AMLAI OC EXPANSION SECTOR B (1.50 MTY) (SOUTH-EASTERN COAL FIELDS LIMITED) - [N06000082]	198.59	03/2016	169.15
144	GOKUL (WESTERN COAL FIELDS LIMITED) - [N06000120]	267.67	03/2018	209.47
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
145	IMPROVEMENT FROM KM 0/0 TO 68/0 EPC(PUBLIC WORKS DEPT OF STATE) - [N24000413]	319.80	10/2016	268.01
146	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000642]	226.31	10/2017	137.43
147	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000643]	319.80	05/2016	268.27
148	WIDENING TO 2L/2LPS FROM 131/0 TO 192/0 (BHOJPUR TO CHHATABAR) OF NH-200 UNDER NHIIP IN ODISHA (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000918]	251.92	10/2015	225.98
149	WIDENING TO 2L/2LPS FROM 25/0 TO 80/0 (NABARANGPUR TO KOKSARA) OF NH-201 UNDER NHIIP IN ODISHA (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000919]	265.35	10/2015	247.56
150	WIDENING TO 2L FROM 228/70 TO 258/70 AND 286/70 TO 327/70 OF VR ROUTE UNDER VRC IN ODISHA (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000924]	229.29	11/2015	163.40
151	REHABILITATION AND UPGRADATION OF EEPURUPALEM-ONGOLE SECTION FROM KM195.000 TO 254.500 OF NH214A(NH2 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS) - [N24000971]	574.19	07/2017	456.98
	September,2019			
	<u>PETROLEUM</u>			
152	URAN CHAKAN SHIKRAPUR LPG PIPELINE (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000155]	309.81	10/2014	712.26
153	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000237]	407.00	09/2019	391.85

TABLE-3

Month wise List of Deleted Projects Costing Rs.150 Crore and above during				
2019-2020				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	June,2019			
	<u>RAILWAYS</u>			
1	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL (RAIL VIKAS NIGAM LTD.) - [220100149]	631.78	12/2012	762.72
2	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR (NORTHERN RAILWAY) - [220100258]	625.30	06/2007	848.84
3	TAMLUK DIGHA,LINE DOUBLING (SER) (SOUTH EASTERN RAILWAY) - [N22000097]	293.97	06/2005	0.00
4	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) (NORTH WESTERN RAILWAY) - [N22000112]	829.74	03/2015	823.85
5	SANTOSH PUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE (EASTERN RAILWAYS) - [N22000248]	268.52	-	0.00
6	MUNIRABAD (GINGERA) -RAICHUR NL (SOUTH WESTERN RAILWAY) - [N22000257]	179.65	-	940.47
7	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL (NORTHERN RAILWAY) - [N22000268]	396.04	-	225.18
8	CHANDIGARH-BADDI NL (NORTHERN RAILWAY) - [N22000296]	328.14	-	233.84
9	MM FROM BURAMARA-CHAKULIA (SOUTH EASTERN RAILWAY) - [N22000305]	466.48	-	0.83
10	MIRAJ-LONDA (SOUTH WESTERN RAILWAY) - [N22000327]	1,830.00	-	254.57
11	CHHINDWARA-MANDLA FORT GC (SOUTH EAST CENTRAL RAILWAY) - [N22000481]	556.54	03/2012	0.00
12	KENDRI-DHAMTARI INCLUDING ABHANPUR-RAJIM (SOUTH EAST CENTRAL RAILWAY) - [N22000482]	1,471.93	03/2022	0.00
	<u>WATER RESOURCES</u>			
13	PAGLADIYA DAM PROJECT (MINISTRY OF WATER RESOURCES) - [300100001]	542.90	12/2007	0.00
	July,2019			
	<u>STEEL</u>			
14	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000085]	188.93	04/2015	138.83
15	REVAMPING OF SINTER MACHINES - 1 AND 2 (RASTRIYA ISPAT NIGAM LIMITED) - [N12000091]	343.00	10/2016	254.65
16	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000097]	4,749.00	09/2017	110.95

Month wise List of Deleted Projects Costing Rs.150 Crore and above during

2019-2020

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
17	2 MTPA PELLET PLANT AT NAGARNAR (NATIONAL MINERAL DEVELOPMENT CORPORATION (NMDC)) - [N12000115]	818.00	06/2020	31.60
	<u>RAILWAYS</u>			
18	BHADUTOLA-JHARGRAM VIA LALGARH (NL) (SOUTH EASTERN RAILWAY) - [N22000161]	289.64	-	0.13
19	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI (NORTHERN RAILWAY) - [N22000270]	654.00	-	0.00
20	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR (NORTHERN RAILWAY) - [N22000271]	1,239.00	-	0.00
21	HISSAR-SIRSA VIA AGROHA AND FATEHABAD (NORTHERN RAILWAY) - [N22000292]	400.00	-	0.00
22	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH (NORTHERN RAILWAY) - [N22000293]	876.00	-	0.00
23	MM FROM PANSKURA-GHATAL NL (SOUTH EASTERN RAILWAY) - [N22000309]	276.69	-	0.00
24	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI(SOUTH EASTERN RAILWAY) - [N22000397]	1,013.45	12/2021	0.01
25	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO(SOUTH EASTERN RAILWAY) - [N22000398]	524.43	12/2021	184.33
	<u>August,2019</u>			
	<u>SHIPPING AND PORTS</u>			
26	SETHUSAMUDRAM SHIP CHANNEL PROJECT (PORT TRUST) - [250100175]	2,427.40	10/2008	0.00
27	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) (PORT TRUST) - [N25000035]	150.00	03/2006	0.00
28	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB(MUMBAI PORT TRUST) - [N25000063]	366.39	12/2010	0.00
29	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED (KAMARAJAR PORT LIMITED) - [N25000066]	244.50	12/2017	0.00
30	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT (KAMARAJAR PORT LIMITED) - [N25000070]	600.00	12/2017	0.00
31	NEW LARGE DRY DOCK AT COCHIN SHIPYARD LIMITED PREMISES AT KOCHI KERALA (COCHIN SHIPYARD LTD) - [N25000073]	1,799.00	05/2021	347.03
32	INTERNATIONAL SHIP REPAIR FACILITY PROJECT AT COCHIN PORT TRUST PREMISES (COCHIN SHIPYARD LTD) - [N25000074]	970.00	05/2020	322.54
	<u>DEFENCE PRODUCTION</u>			
33	CONSTRUCTION WORKS PHASE 4 (GOA SHIPYARD LIMITED) - [N39000001]	167.69	05/2018	141.83
34	CONSTRUCTION WORKS PHASE 3B (GOA SHIPYARD LIMITED) - [N39000002]	285.95	08/2020	84.40

TABLE-4

Projects Added / Completed / Dropped / Frozen Rs.150 Crore and above

No of Projects in Previous Month	1634
No of Projects Completed/Dropped/Frozen in Current Month	2
No of Projects Elevated in Current Month	2
No of Projects added in Current Month	1
No of Projects in Current Month	1635

Project status Rs.150 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	565 (34.56%)	24 (1.47%)	353(21.59%)	176 (10.76%)	517(1.62%)	1635
Latest Approved (Date)	495 (30.28%)	29 (1.77%)	446(27.28%)	140 (8.56%)	525(2.11%)	1635

Project cost Rs.150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	1311	16,07,187.95	18,36,552.04	7,20,172.70	39.20	2,29,364.09	14.30
Project with Revision in Cost	324	5,14,090.22	5,05,481.35	2,76,441.24	54.70	-8,608.87	-1.70
Total	1,635	21,21,029.62	23,41,784.84	9,96,613.94	42.55	2,20,755.22	10.41
Original Cost of All Projects							
Original Cost	1,635	19,47,462.67	23,41,784.84	9,96,613.94	42.55	3,94,322.17	20.25

Delayed Project cost Rs.150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	565	8,45,560.27	10,81,723.56	5,64,991.94	52.20	2,36,163.29	27.93
Latest Approved (RCE)	495	7,36,841.89	8,60,998.43	4,07,740.91	47.40	1,24,156.54	16.85
Additional Delayed Project cost Rs.150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Latest Approved	59	66,373.61	77,466.00	43,612.55	56.30	11,092.39	16.70
Total	59	66,373.61	77,466.00	43,612.55	56.30	11,092.39	16.71


Summary of projects in the Flash Report for the month of September, 2019

Project Implementation - Current Status:

Number of Projects in Previous Month	1634
Number of Projects completed/dropped/frozen in Current Month	2
Number of Projects elevated to the status of Major project during the current month	2
Number of Projects Added in Current Month	1
Number of Projects in Current Month	1635

Brief Analysis

Project Status with respect to Original Schedule: Out of 1635 projects, 24 projects are ahead of schedule, 353 projects are on schedule 565 projects are delayed. 517 projects do not have fixed dates of commissioning. 176 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

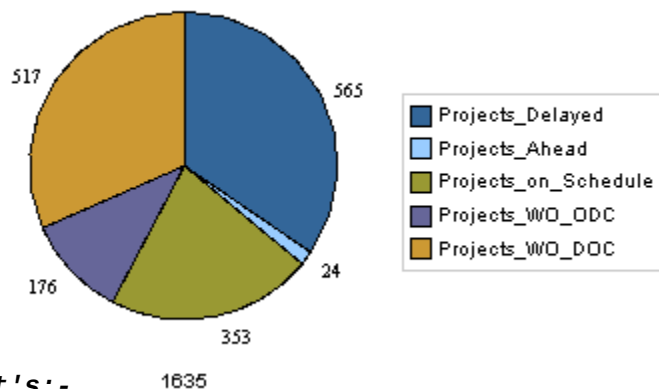

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1635 projects when sanctioned, was of the order of Rs. 1947711.22 crore but this was subsequently revised to Rs. 2342033.39 crore implying a cost overrun of 20.2%. The expenditure incurred on these projects till September, 2019 is Rs. 996613.94 crore, which is 42.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

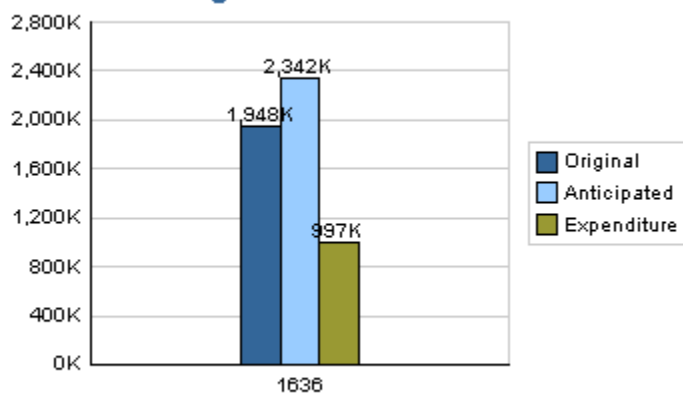


TABLE-5

Extent of cost overrun in projects with respect to original schedule(Sector Wise) Rs.150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	48.51
2	CIVIL AVIATION	13	8,607.51	8,734.44	1.47	3	1,513.40	1,640.33	8.39
3	COAL	107	1,04,997.33	1,07,975.18	2.84	12	28,387.67	33,223.79	17.04
4	FERTILISERS	5	1,299.07	1,310.72	0.90	1	197.79	209.44	5.89
5	INFORMATION AND BROADCASTING	3	969.43	969.43	0.00	0	0.00	0.00	0.00
6	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	0.00
7	STEEL	9	26,228.23	33,485.23	27.67	1	15,525.00	23,140.00	49.05
8	PETROLEUM	150	2,45,939.08	2,53,886.39	3.23	27	43,862.64	54,016.41	23.15
9	POWER	76	2,85,786.68	3,59,673.67	25.85	30	1,54,828.95	2,29,232.99	48.06
10	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0.00
11	HEALTH AND FAMILY WELFARE	21	9,480.23	9,597.52	1.24	3	1,076.25	1,193.54	10.90
12	RAILWAYS	315	4,61,117.38	6,64,220.06	44.05	187	1,78,466.58	3,92,821.78	120.11
13	ROAD TRANSPORT AND HIGHWAYS	856	5,09,942.21	5,31,171.55	4.16	92	63,969.35	89,108.69	39.30
14	SHIPPING AND PORTS	1	4,200.00	5,369.18	27.84	1	4,200.00	5,369.18	27.84
15	TELECOMMUNICATIONS	4	16,095.23	27,333.53	69.82	2	13,565.80	24,904.10	83.58
16	URBAN DEVELOPMENT	63	1,86,663.06	1,93,294.88	3.55	14	29,058.09	35,689.91	22.82
17	WATER RESOURCES	2	10,384.61	55,782.44	437.16	1	10,151.04	55,548.87	447.22
Total		1635	19,47,462.67	23,41,784.84	20.25	377	5,72,073.56	9,86,598.03	72.46

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-6

Extent of cost overrun in projects with respect to original schedule(State Wise) Rs.150 Crore and above (All Cost/ Expenditure in Rs. Crore)									
						Projects with cost overrun [^]			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	74	1,19,083.46	1,68,703.11	41.67	12	21,568.57	72,050.08	234.05
2	ARUNACHAL PRADESH	40	21,795.08	40,754.39	86.99	5	9,284.82	28,244.13	204.20
3	ASSAM	48	26,216.03	31,003.54	18.26	18	6,570.68	11,631.28	77.02
4	BIHAR	94	90,608.62	1,27,798.63	41.04	30	38,346.70	75,612.34	97.18
5	GOA	10	5,325.87	5,336.30	0.20	1	280.16	290.59	3.72
6	GUJARAT	56	64,665.47	71,921.79	11.22	10	18,114.14	25,526.79	40.92
7	HARYANA	40	30,880.96	33,054.71	7.04	5	3,330.78	5,915.01	77.59
8	HIMACHAL PRADESH	13	18,053.17	28,163.70	56.00	2	6,886.58	16,997.11	146.82
9	JAMMU AND KASHMIR	13	20,822.23	46,498.48	123.31	2	4,659.00	30,468.00	553.96
10	KARNATAKA	63	73,084.28	76,598.88	4.81	15	13,979.23	18,026.26	28.95
11	KERALA	20	36,309.60	39,755.52	9.49	9	16,705.01	20,346.47	21.80
12	MADHYA PRADESH	78	86,555.71	93,301.25	7.79	9	28,541.25	37,229.83	30.44
13	MAHARASHTRA	258	2,36,169.10	2,46,235.56	4.26	35	42,158.12	57,511.15	36.42
14	MANIPUR	5	6,002.36	14,012.39	133.45	1	4,454.17	12,524.00	181.17
15	MEGHALAYA	6	2,760.77	7,854.31	184.50	1	906.46	6,000.00	561.92
16	MIZORAM	13	7,757.62	11,189.69	44.24	5	3,593.57	7,025.64	95.51
17	NAGALAND	26	14,842.43	17,115.91	15.32	1	2,326.52	4,600.00	97.72
18	ODISHA	92	1,06,784.06	1,09,220.71	2.28	17	27,343.52	33,359.70	22.00
19	PUNJAB	27	13,539.35	15,038.78	11.07	5	3,867.41	5,421.60	40.19
20	RAJASTHAN	63	47,345.31	54,833.78	15.82	13	17,425.66	24,914.13	42.97
21	SIKKIM	9	3,476.73	6,368.17	83.17	3	1,909.76	4,801.20	151.40
22	TAMIL NADU	65	1,16,109.47	1,34,527.19	15.86	23	39,899.68	59,915.02	50.16
23	TRIPURA	7	1,977.29	2,139.55	8.21	5	1,436.39	1,598.65	11.30
24	UTTAR PRADESH	118	1,44,722.96	1,49,516.00	3.31	19	39,319.51	46,140.00	17.35
25	WEST BENGAL	64	59,103.95	73,911.74	25.05	22	23,918.62	39,062.71	63.32
26	A & N ISLANDS	9	2,786.01	2,893.59	3.86	2	552.41	679.33	22.98
27	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	0.00
28	DELHI	25	55,985.34	63,868.57	14.08	6	6,981.71	14,864.94	112.91
29	CHHATISGARH	34	73,625.10	85,279.62	15.83	8	34,846.39	46,931.47	34.68
30	JHARKHAND	47	62,036.07	67,344.06	8.56	9	23,217.46	28,529.23	22.88
31	UTTARAKHAND	31	35,661.33	44,552.75	24.93	9	10,197.17	19,115.09	87.45
32	TELANGANA	56	39,959.69	42,435.36	6.20	11	5,987.17	9,116.11	52.26
33	MULTI STATE	130	3,17,331.17	4,24,714.50	33.84	64	1,13,464.94	2,22,150.17	95.79
Total		1635	19,47,462.67	23,41,784.84	20.25	377	5,72,073.56	9,86,598.03	72.46

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-7

Extent of time overrun in projects with respect to original schedule Rs.150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	4	67,120.00	80,348.00	36 - 133
2	CIVIL AVIATION	13	8,607.51	8,734.44	1.47	5	3,573.83	3,700.62	6 - 21
3	COAL	107	1,04,997.33	1,07,975.18	2.84	37	18,538.74	20,501.47	12 - 144
4	FERTILISERS	5	1,299.07	1,310.72	0.90	1	197.79	209.44	34 - 34
5	INFORMATION AND BROADCASTING	3	969.43	969.43	0.00	1	204.32	204.32	9 - 9
6	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	-
7	STEEL	9	26,228.23	33,485.23	27.67	8	25,964.87	33,221.87	12 - 62
8	PETROLEUM	150	2,45,939.08	2,53,886.39	3.23	52	1,13,827.55	1,18,174.58	1 - 110
9	POWER	76	2,85,786.68	3,59,673.67	25.85	49	1,75,240.00	2,34,057.76	5 - 147
10	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	-
11	HEALTH AND FAMILY WELFARE	21	9,480.23	9,597.52	1.24	10	4,400.02	4,499.80	2 - 83
12	RAILWAYS	315	4,61,117.38	6,64,220.06	44.05	146	1,80,706.42	2,65,634.96	1 - 324
13	ROAD TRANSPORT AND HIGHWAYS	856	5,09,942.21	5,31,171.55	4.16	225	1,39,959.97	1,47,056.07	1 - 149
14	SHIPPING AND PORTS	1	4,200.00	5,369.18	27.84	0	0.00	0.00	-
15	TELECOMMUNICATIONS	4	16,095.23	27,333.53	69.82	2	13,565.80	24,904.10	14 - 58
16	URBAN DEVELOPMENT	63	1,86,663.06	1,93,294.88	3.55	24	92,109.92	93,661.70	2 - 89
17	WATER RESOURCES	2	10,384.61	55,782.44	437.16	1	10,151.04	55,548.87	15 - 15
Total		1635	19,47,462.67	23,41,784.84	20.25	565	8,45,560.27	10,81,723.56	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-8

Extent of time overrun in projects with respect to original schedule(State Wise) Rs.150 Crore and above

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	74	1,19,083.46	1,68,703.11	41.67	38	70,253.04	1,17,144.23	1 - 168
2	ARUNACHAL PRADESH	40	21,795.08	40,754.39	86.99	10	5,497.90	10,944.41	21 - 118
3	ASSAM	48	26,216.03	31,003.54	18.26	18	9,558.51	11,266.33	1 - 149
4	BIHAR	94	90,608.62	1,27,798.63	41.04	18	36,621.31	62,026.21	6 - 118
5	GOA	10	5,325.87	5,336.30	0.20	0	0.00	0.00	-
6	GUJARAT	56	64,665.47	71,921.79	11.22	17	35,046.73	41,291.13	2 - 120
7	HARYANA	40	30,880.96	33,054.71	7.04	10	7,716.19	9,850.32	1 - 118
8	HIMACHAL PRADESH	13	18,053.17	28,163.70	56.00	4	7,610.81	13,688.33	15 - 147
9	JAMMU AND KASHMIR	13	20,822.23	46,498.48	123.31	5	9,893.33	35,342.33	18 - 235
10	KARNATAKA	63	73,084.28	76,598.88	4.81	25	49,707.17	51,430.75	3 - 264
11	KERALA	20	36,309.60	39,755.52	9.49	9	17,162.14	18,898.34	8 - 89
12	MADHYA PRADESH	78	86,555.71	93,301.25	7.79	34	32,889.55	38,626.73	2 - 54
13	MAHARASHTRA	258	2,36,169.10	2,46,235.56	4.26	79	1,15,943.15	1,18,605.82	1 - 204
14	MANIPUR	5	6,002.36	14,012.39	133.45	3	5,188.43	13,198.46	36 - 108
15	MEGHALAYA	6	2,760.77	7,854.31	184.50	2	843.19	843.19	16 - 17
16	MIZORAM	13	7,757.62	11,189.69	44.24	5	3,593.57	7,025.64	63 - 116
17	NAGALAND	26	14,842.43	17,115.91	15.32	2	2,723.04	4,996.52	46 - 79
18	ODISHA	92	1,06,784.06	1,09,220.71	2.28	38	49,395.23	51,822.52	3 - 183
19	PUNJAB	27	13,539.35	15,038.78	11.07	7	3,169.78	3,570.93	1 - 29
20	RAJASTHAN	63	47,345.31	54,833.78	15.82	19	22,255.60	27,919.61	1 - 48
21	SIKKIM	9	3,476.73	6,368.17	83.17	2	333.87	420.73	76 - 82
22	TAMIL NADU	65	1,16,109.47	1,34,527.19	15.86	23	68,434.13	76,973.98	5 - 133
23	TRIPURA	7	1,977.29	2,139.55	8.21	3	1,277.56	1,358.00	6 - 21
24	UTTAR PRADESH	118	1,44,722.96	1,49,516.00	3.31	35	47,768.66	51,939.39	2 - 70
25	WEST BENGAL	64	59,103.95	73,911.74	25.05	28	32,526.06	39,761.45	4 - 324
26	A & N ISLANDS	9	2,786.01	2,893.59	3.86	1	314.61	441.33	21 - 21
27	D & N HAVELI	1	6,086.08	5,842.31	-4.01	1	6,086.08	5,842.31	5 - 5
28	DELHI	25	55,985.34	63,868.57	14.08	7	3,932.68	4,813.25	3 - 83
29	CHHATISGARH	34	73,625.10	85,279.62	15.83	14	39,819.26	50,888.18	3 - 84
30	JHARKHAND	47	62,036.07	67,344.06	8.56	17	21,973.06	23,368.28	9 - 120
31	UTTARAKHAND	31	35,661.33	44,552.75	24.93	10	25,218.73	33,623.06	3 - 114
32	TELANGANA	56	39,959.69	42,435.36	6.20	23	20,665.97	21,002.46	5 - 156
33	MULTI STATE	130	3,17,331.17	4,24,714.50	33.84	58	92,140.93	1,32,799.34	5 - 252
Total		1635	19,47,462.67	23,41,784.84	20.25	565	8,45,560.27	10,81,723.56	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-9

Extent of time overrun in projects with respect to latest schedule Rs.150 Crore and above									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	77,000.00	80,348.00	4.35	4	77,000.00	80,348.00	36 - 133
2	CIVIL AVIATION	13	8,607.51	8,734.44	1.47	5	3,573.83	3,700.62	6 - 21
3	COAL	107	1,06,170.63	1,07,975.18	1.70	38	19,984.77	20,774.20	0 - 144
4	FERTILISERS	5	1,299.07	1,310.72	0.90	1	197.79	209.44	34 - 34
5	INFORMATION AND BROADCASTING	3	969.43	969.43	0.00	1	204.32	204.32	9 - 9
6	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	-
7	STEEL	9	26,228.23	33,485.23	27.67	0	0.00	0.00	-
8	PETROLEUM	150	2,52,707.26	2,53,886.39	0.47	33	69,843.64	70,115.60	1 - 110
9	POWER	76	3,11,064.60	3,59,673.67	15.63	41	1,08,758.17	1,37,540.97	5 - 147
10	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	-
11	HEALTH AND FAMILY WELFARE	21	9,480.23	9,597.52	1.24	10	4,400.02	4,499.80	2 - 83
12	RAILWAYS	315	5,68,328.18	6,64,220.06	16.87	128	1,99,796.30	2,39,305.07	1 - 264
13	ROAD TRANSPORT AND HIGHWAYS	856	5,31,478.79	5,31,171.55	-0.06	209	1,48,577.74	1,41,677.21	0 - 149
14	SHIPPING AND PORTS	1	5,369.18	5,369.18	0.00	0	0.00	0.00	-
15	TELECOMMUNICATIONS	4	16,103.53	27,333.53	69.74	1	13,334.00	24,664.00	58 - 58
16	URBAN DEVELOPMENT	63	1,87,205.75	1,93,294.88	3.25	23	81,020.27	82,410.33	0 - 89
17	WATER RESOURCES	2	10,384.61	55,782.44	437.16	1	10,151.04	55,548.87	15 - 15
Total		1635	21,21,029.62	23,41,784.84	10.41	495	7,36,841.89	8,60,998.43	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-10

Extent of cost overrun in projects with respect to latest schedule RS.150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	77,000.00	80,348.00	4.35	1	3,492.00	6,840.00	95.88
2	CIVIL AVIATION	13	8,607.51	8,734.44	1.47	3	1,513.40	1,640.33	8.39
3	COAL	107	1,06,170.63	1,07,975.18	1.70	11	22,480.56	26,143.38	16.29
4	FERTILISERS	5	1,299.07	1,310.72	0.90	1	197.79	209.44	5.89
5	INFORMATION AND BROADCASTING	3	969.43	969.43	0.00	0	0.00	0.00	0.00
6	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	0.00
7	STEEL	9	26,228.23	33,485.23	27.67	1	15,525.00	23,140.00	49.05
8	PETROLEUM	150	2,52,707.26	2,53,886.39	0.47	13	16,950.80	20,051.58	18.29
9	POWER	76	3,11,064.60	3,59,673.67	15.63	26	1,27,696.04	1,76,822.16	38.47
10	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0.00
11	HEALTH AND FAMILY WELFARE	21	9,480.23	9,597.52	1.24	3	1,076.25	1,193.54	10.90
12	RAILWAYS	315	5,68,328.18	6,64,220.06	16.87	158	1,41,728.44	2,47,460.54	74.60
13	ROAD TRANSPORT AND HIGHWAYS	856	5,31,478.79	5,31,171.55	-0.06	104	58,808.85	78,315.06	33.17
14	SHIPPING AND PORTS	1	5,369.18	5,369.18	0.00	0	0.00	0.00	0.00
15	TELECOMMUNICATIONS	4	16,103.53	27,333.53	69.74	1	13,334.00	24,664.00	84.97
16	URBAN DEVELOPMENT	63	1,87,205.75	1,93,294.88	3.25	10	28,341.60	34,430.73	21.48
17	WATER RESOURCES	2	10,384.61	55,782.44	437.16	1	10,151.04	55,548.87	447.22
Total		1635	21,21,029.62	23,41,784.84	10.41	333	4,41,295.77	6,96,459.63	57.82

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-11

Extent of time & cost overrun in projects with respect to latest schedule Rs.150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	77,000.00	80,348.00	4.35	1	3,492.00	6,840.00	133- 133
2	CIVIL AVIATION	13	8,607.51	8,734.44	1.47	2	653.54	780.33	6- 21
3	COAL	107	1,06,170.63	1,07,975.18	1.70	8	2,393.89	3,309.66	12- 144
4	FERTILISERS	5	1,299.07	1,310.72	0.90	1	197.79	209.44	34- 34
5	INFORMATION AND BROADCASTING	3	969.43	969.43	0.00	0	0.00	0.00	0- 0
6	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	0- 0
7	STEEL	9	26,228.23	33,485.23	27.67	0	0.00	0.00	0- 0
8	PETROLEUM	150	2,52,707.26	2,53,886.39	0.47	4	4,392.47	4,792.21	4- 110
9	POWER	76	3,11,064.60	3,59,673.67	15.63	15	68,913.25	97,696.05	21- 147
10	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0- 0
11	HEALTH AND FAMILY WELFARE	21	9,480.23	9,597.52	1.24	1	414.11	513.89	83- 83
12	RAILWAYS	315	5,68,328.18	6,64,220.06	16.87	65	65,007.37	1,10,055.79	6- 252
13	ROAD TRANSPORT AND HIGHWAYS	856	5,31,478.79	5,31,171.55	-0.06	32	19,009.53	24,154.33	1- 143
14	SHIPPING AND PORTS	1	5,369.18	5,369.18	0.00	0	0.00	0.00	0- 0
15	TELECOMMUNICATIONS	4	16,103.53	27,333.53	69.74	1	13,334.00	24,664.00	58- 58
16	URBAN DEVELOPMENT	63	1,87,205.75	1,93,294.88	3.25	4	7,285.00	8,675.06	17- 40
17	WATER RESOURCES	2	10,384.61	55,782.44	437.16	1	10,151.04	55,548.87	15- 15
Total		1635	21,21,029.62	23,41,784.84	10.41	135	1,95,243.99	3,37,239.63	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-12

Extent of time & cost overrun in projects with respect to original schedule Rs.150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	48- 133
2	CIVIL AVIATION	13	8,607.51	8,734.44	1.47	2	653.54	780.33	6- 21
3	COAL	107	1,04,997.33	1,07,975.18	2.84	9	8,301.00	10,390.07	12- 144
4	FERTILISERS	5	1,299.07	1,310.72	0.90	1	197.79	209.44	34- 34
5	INFORMATION AND BROADCASTING	3	969.43	969.43	0.00	0	0.00	0.00	0- 0
6	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	0- 0
7	STEEL	9	26,228.23	33,485.23	27.67	1	15,525.00	23,140.00	62- 62
8	PETROLEUM	150	2,45,939.08	2,53,886.39	3.23	16	29,947.50	35,561.59	1- 110
9	POWER	76	2,85,786.68	3,59,673.67	25.85	23	1,30,663.48	1,89,481.24	21- 147
10	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0- 0
11	HEALTH AND FAMILY WELFARE	21	9,480.23	9,597.52	1.24	1	414.11	513.89	83- 83
12	RAILWAYS	315	4,61,117.38	6,64,220.06	44.05	85	83,601.46	1,77,486.48	3- 324
13	ROAD TRANSPORT AND HIGHWAYS	856	5,09,942.21	5,31,171.55	4.16	37	24,756.06	33,472.90	1- 143
14	SHIPPING AND PORTS	1	4,200.00	5,369.18	27.84	0	0.00	0.00	0- 0
15	TELECOMMUNICATIONS	4	16,095.23	27,333.53	69.82	2	13,565.80	24,904.10	14- 58
16	URBAN DEVELOPMENT	63	1,86,663.06	1,93,294.88	3.55	6	7,948.75	9,500.53	7- 70
17	WATER RESOURCES	2	10,384.61	55,782.44	437.16	1	10,151.04	55,548.87	15- 15
Total		1635	19,47,462.67	23,41,784.84	20.25	187	3,52,996.53	6,01,488.44	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-13

State-Wise Position of Central Sector Projects costing Rs.150 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	74	1,19,083.46	1,68,703.11	41.67	6	14,338.19	61,946.02	1 - 168
2	ARUNACHAL PRADESH	40	21,795.08	40,754.39	86.99	2	2,635.83	8,082.34	36 - 118
3	ASSAM	48	26,216.03	31,003.54	18.26	5	1,654.05	3,518.82	4 - 143
4	BIHAR	94	90,608.62	1,27,798.63	41.04	10	30,865.91	56,278.52	12 - 118
5	GOA	10	5,325.87	5,336.30	0.20	0	0.00	0.00	-
6	GUJARAT	56	64,665.47	71,921.79	11.22	5	13,479.15	19,879.88	12 - 120
7	HARYANA	40	30,880.96	33,054.71	7.04	2	1,395.00	3,661.50	100 - 111
8	HIMACHAL PRADESH	13	18,053.17	28,163.70	56.00	1	3,919.59	9,997.11	147 - 147
9	JAMMU AND KASHMIR	13	20,822.23	46,498.48	123.31	1	2,500.00	27,949.00	235 - 235
10	KARNATAKA	63	73,084.28	76,598.88	4.81	7	6,263.21	8,300.22	3 - 36
11	KERALA	20	36,309.60	39,755.52	9.49	5	12,261.94	14,022.18	15 - 33
12	MADHYA PRADESH	78	86,555.71	93,301.25	7.79	6	17,231.95	23,065.44	6 - 36
13	MAHARASHTRA	258	2,36,169.10	2,46,235.56	4.26	21	24,595.79	32,413.31	1 - 204
14	MANIPUR	5	6,002.36	14,012.39	133.45	1	4,454.17	12,524.00	108 - 108
15	MEGHALAYA	6	2,760.77	7,854.31	184.50	0	0.00	0.00	-
16	MIZORAM	13	7,757.62	11,189.69	44.24	5	3,593.57	7,025.64	63 - 116
17	NAGALAND	26	14,842.43	17,115.91	15.32	1	2,326.52	4,600.00	79 - 79
18	ODISHA	92	1,06,784.06	1,09,220.71	2.28	14	24,067.16	29,994.02	3 - 183
19	PUNJAB	27	13,539.35	15,038.78	11.07	3	1,589.83	1,990.98	1 - 29
20	RAJASTHAN	63	47,345.31	54,833.78	15.82	7	14,217.88	19,881.89	6 - 48
21	SIKKIM	9	3,476.73	6,368.17	83.17	1	182.28	269.14	82 - 82
22	TAMIL NADU	65	1,16,109.47	1,34,527.19	15.86	7	15,872.04	24,411.89	12 - 133
23	TRIPURA	7	1,977.29	2,139.55	8.21	2	908.56	989.00	6 - 21
24	UTTAR PRADESH	118	1,44,722.96	1,49,516.00	3.31	8	14,750.30	19,482.81	5 - 70
25	WEST BENGAL	64	59,103.95	73,911.74	25.05	11	16,382.67	23,633.10	12 - 324
26	A & N ISLANDS	9	2,786.01	2,893.59	3.86	1	314.61	441.33	21 - 21
27	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	-
28	DELHI	25	55,985.34	63,868.57	14.08	2	1,633.32	2,513.89	17 - 83
29	CHHATISGARH	34	73,625.10	85,279.62	15.83	6	32,944.43	44,443.91	9 - 62
30	JHARKHAND	47	62,036.07	67,344.06	8.56	4	16,497.75	17,892.97	9 - 36
31	UTTARAKHAND	31	35,661.33	44,552.75	24.93	5	7,847.16	16,277.99	19 - 114
32	TELANGANA	56	39,959.69	42,435.36	6.20	7	3,574.19	4,563.95	12 - 144
33	MULTI STATE	130	3,17,331.17	4,24,714.50	33.84	31	60,699.48	1,01,437.59	8 - 240
Total		1635	19,47,462.67	23,41,784.84	20.25	187	3,52,996.53	6,01,488.44	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-14

EXECUTIVE SUMMARY COSTING Rs.1000 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	156	8
2	ROAD TRANSPORT AND HIGHWAYS	149	5
3	PETROLEUM	56	3
4	POWER	43	4
5	COAL	16	1
6	URBAN DEVELOPMENT	16	0
7	STEEL	6	1
8	ATOMIC ENERGY	4	0
9	CIVIL AVIATION	2	0
10	TELECOMMUNICATIONS	2	0
11	MINES	1	0
12	HEAVY INDUSTRY	1	0
13	HEALTH AND FAMILY WELFARE	1	0
14	SHIPPING AND PORTS	1	0
15	WATER RESOURCES	1	0
	Total	455	22

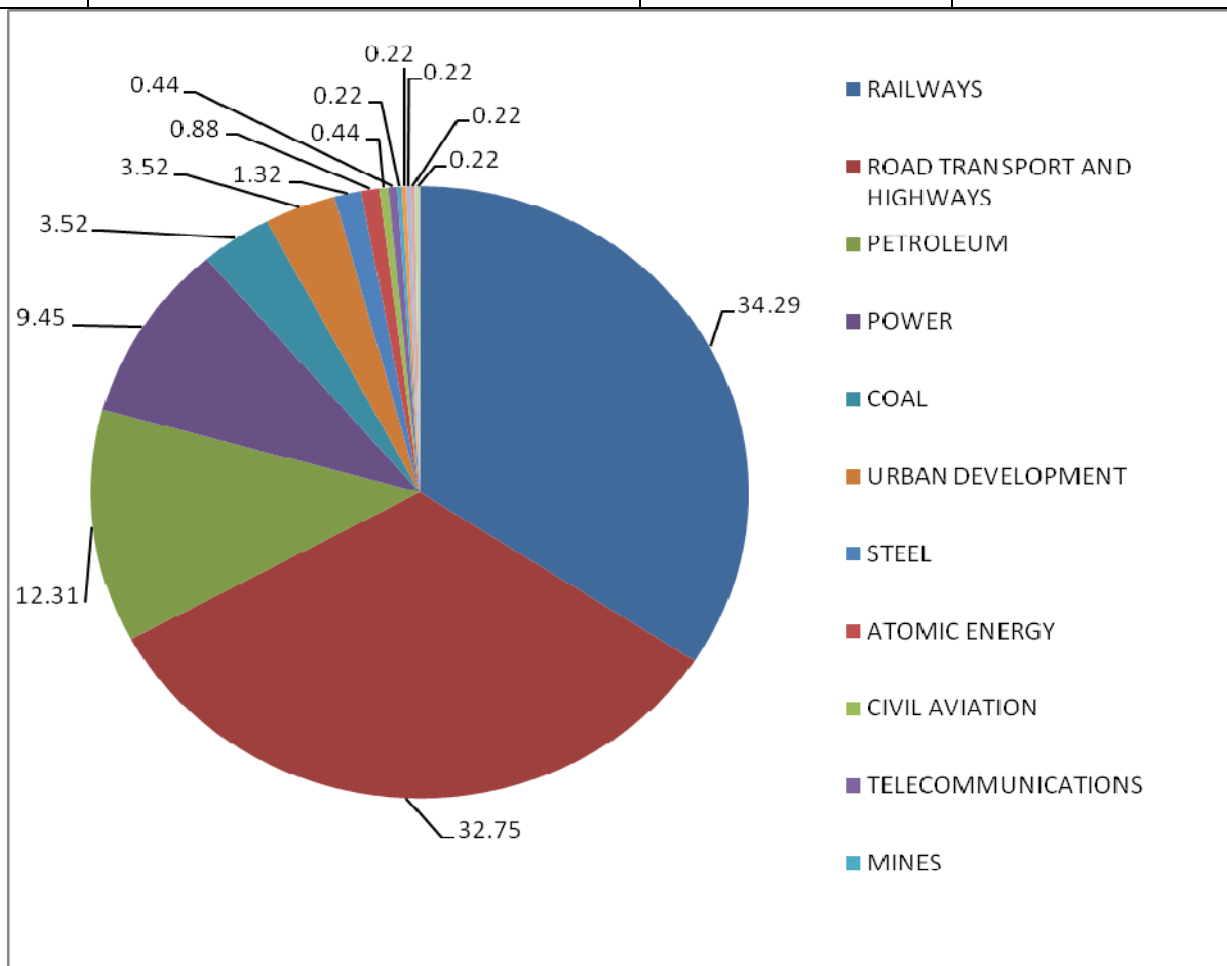


TABLE-15

Projects Added / Completed / Dropped / Frozen Rs. 1000 Crore and above

No of Projects in Previous Month	453
No of Projects Completed/Dropped/Frozen in Current Month	0
No of Projects added in Current Month	1
No of Projects in Current Month	455

Project status Rs.1000 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	197 (43.30%)	7 (1.54%)	89 (19.56%)	54 (11.87%)	108(3.74%)	455
Latest Approved (Date)	162 (35.60%)	8 (1.76%)	130(28.57%)	44 (9.67%)	111(4.40%)	455

Project cost Rs.1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	360	12,14,872.24	14,32,653.22	5,60,322.13	39.10	2,17,780.98	17.90
Project with Revision in Cost	95	4,15,407.67	4,11,846.76	2,31,584.33	56.20	-3,560.91	-.90
Total	455	16,30,279.91	18,44,499.98	7,91,906.46	42.93	2,14,220.07	13.14
Original Cost of All Projects							
Original Cost	455	14,65,045.87	18,44,499.98	7,91,906.46	42.93	3,79,454.11	25.90

Delayed Project cost Rs.1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	197	6,90,261.18	9,21,069.06	4,83,036.64	52.40	2,30,807.88	33.44
Latest Approved (RCE)	162	5,93,016.18	7,16,419.28	3,34,792.19	46.70	1,23,403.10	20.81

Additional Delayed Project cost Rs.1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Latest Approved	22	52,307.35	62,450.72	34,635.77	55.50	10,143.37	19.40
Total	22	52,307.35	62,450.72	34,635.77	55.46	10,143.37	19.39

TABLE-16

Extent of cost overrun in projects with respect to original schedule(Sector Wise) Rs.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	48.51
2	CIVIL AVIATION	2	3,850.00	3,850.00	0.00	0	0.00	0.00	0.00
3	COAL	16	66,016.48	69,715.09	5.60	3	25,805.84	29,504.45	14.33
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
5	STEEL	6	25,381.34	32,638.34	28.59	1	15,525.00	23,140.00	49.05
6	PETROLEUM	56	2,06,905.35	2,14,210.01	3.53	16	38,761.90	48,089.93	24.06
7	POWER	43	2,72,525.71	3,45,979.95	26.95	24	1,52,955.09	2,26,926.38	48.36
8	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0.00
9	HEALTH AND FAMILY WELFARE	1	1,351.00	1,351.00	0.00	0	0.00	0.00	0.00
10	RAILWAYS	156	3,92,689.00	5,84,806.59	48.92	98	1,47,361.38	3,45,010.98	134.13
11	ROAD TRANSPORT AND HIGHWAYS	149	2,19,449.56	2,37,782.08	8.35	30	40,634.62	59,269.07	45.86
12	SHIPPING AND PORTS	1	4,200.00	5,369.18	27.84	1	4,200.00	5,369.18	27.84
13	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	84.97
14	URBAN DEVELOPMENT	16	1,72,867.22	1,79,131.70	3.62	5	26,033.88	32,298.36	24.06
15	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	447.22
Total		455	14,65,045.87	18,44,499.98	25.90	183	5,02,033.75	8,90,320.22	77.34

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-17

Extent of cost overrun in projects with respect to original schedule(State Wise) Rs.1000 Crore and above (All Cost/ Expenditure in Rs. Crore)									
						Projects with cost overrun [^]			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	21	98,791.39	1,48,859.72	50.68	8	20,509.81	70,936.14	245.86
2	ARUNACHAL PRADESH	5	13,732.92	32,374.37	135.74	2	8,782.23	27,423.68	212.26
3	ASSAM	8	11,678.49	14,282.38	22.30	3	2,127.51	4,868.01	128.81
4	BIHAR	24	58,587.95	92,937.56	58.63	13	31,489.79	65,839.40	109.08
5	GUJARAT	18	46,707.74	53,208.72	13.92	5	16,441.81	22,942.79	39.54
6	HARYANA	11	16,490.84	18,350.34	11.28	1	1,108.00	2,967.50	167.82
7	HIMACHAL PRADESH	7	15,497.19	25,607.72	65.24	2	6,886.58	16,997.11	146.82
8	JAMMU AND KASHMIR	9	19,625.43	45,301.68	130.83	2	4,659.00	30,468.00	553.96
9	KARNATAKA	19	55,423.75	58,665.63	5.85	8	10,837.45	14,275.34	31.72
10	KERALA	9	30,871.86	34,193.65	10.76	6	14,996.96	18,342.79	22.31
11	MADHYA PRADESH	20	58,498.57	66,286.10	13.31	8	28,044.20	36,348.78	29.61
12	MAHARASHTRA	52	1,54,949.73	1,67,635.94	8.19	19	36,356.65	49,814.73	37.02
13	MANIPUR	1	4,454.17	12,524.00	181.17	1	4,454.17	12,524.00	181.17
14	MEGHALAYA	1	906.46	6,000.00	561.92	1	906.46	6,000.00	561.92
15	MIZORAM	1	2,393.47	5,021.45	109.80	1	2,393.47	5,021.45	109.80
16	NAGALAND	3	7,896.52	10,170.00	28.79	1	2,326.52	4,600.00	97.72
17	ODISHA	34	82,737.16	84,721.70	2.40	10	25,048.54	30,532.65	21.89
18	PUNJAB	3	3,627.54	4,765.00	31.36	1	1,388.34	2,525.80	81.93
19	RAJASTHAN	11	24,061.71	30,204.75	25.53	3	14,015.71	20,158.75	43.83
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	204.95
21	TAMIL NADU	25	97,234.18	1,13,562.51	16.79	13	36,705.21	53,730.54	46.38
22	UTTAR PRADESH	42	1,11,806.06	1,16,702.16	4.38	9	35,631.09	41,468.32	16.38
23	WEST BENGAL	24	43,267.91	57,073.09	31.91	11	19,902.61	33,738.83	69.52
24	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	0.00
25	DELHI	7	50,481.91	58,224.75	15.34	3	6,254.39	13,997.23	123.80
26	CHHATISGARH	14	65,083.62	76,559.62	17.63	7	34,693.96	46,471.98	33.95
27	JHARKHAND	13	49,100.48	53,989.92	9.96	5	21,821.72	26,711.16	22.41
28	UTTARAKHAND	7	27,696.84	36,133.38	30.46	4	8,654.06	17,090.60	97.49
29	TELANGANA	5	18,567.06	20,644.30	11.19	2	2,378.60	4,455.84	87.33
30	MULTI STATE	59	2,87,449.36	3,90,572.54	35.88	33	1,01,879.43	2,05,984.11	102.18
Total		455	14,65,045.87	18,44,499.98	25.90	183	5,02,033.75	8,90,320.22	77.34

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-18

Extent of time overrun in projects with respect to original schedule Rs.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	4	67,120.00	80,348.00	36 - 133
2	CIVIL AVIATION	2	3,850.00	3,850.00	0.00	1	2,467.00	2,467.00	6 - 6
3	COAL	16	66,016.48	69,715.09	5.60	2	6,962.16	8,135.46	31 - 48
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	-
5	STEEL	6	25,381.34	32,638.34	28.59	6	25,381.34	32,638.34	13 - 62
6	PETROLEUM	56	2,06,905.35	2,14,210.01	3.53	23	1,02,339.87	1,06,365.04	1 - 110
7	POWER	43	2,72,525.71	3,45,979.95	26.95	27	1,66,076.95	2,24,562.74	7 - 147
8	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	-
9	HEALTH AND FAMILY WELFARE	1	1,351.00	1,351.00	0.00	0	0.00	0.00	-
10	RAILWAYS	156	3,92,689.00	5,84,806.59	48.92	83	1,48,404.65	2,30,936.05	3 - 324
11	ROAD TRANSPORT AND HIGHWAYS	149	2,19,449.56	2,37,782.08	8.35	42	61,209.03	67,301.63	1 - 100
12	SHIPPING AND PORTS	1	4,200.00	5,369.18	27.84	0	0.00	0.00	-
13	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58 - 58
14	URBAN DEVELOPMENT	16	1,72,867.22	1,79,131.70	3.62	7	86,815.14	88,101.93	2 - 64
15	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	15 - 15
Total		455	14,65,045.87	18,44,499.98	25.90	197	6,90,261.18	9,21,069.06	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-19
Extent of time overrun in projects with respect to original schedule(State Wise) Rs.1000 Crore and above

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	21	98,791.39	1,48,859.72	50.68	10	59,598.89	1,06,825.54	1 - 168
2	ARUNACHAL PRADESH	5	13,732.92	32,374.37	135.74	2	3,750.00	9,180.44	60 - 118
3	ASSAM	8	11,678.49	14,282.38	22.30	3	4,072.35	5,132.86	5 - 81
4	BIHAR	24	58,587.95	92,937.56	58.63	9	32,035.52	56,900.64	12 - 118
5	GUJARAT	18	46,707.74	53,208.72	13.92	7	30,986.43	36,587.92	2 - 54
6	HARYANA	11	16,490.84	18,350.34	11.28	2	4,637.00	6,496.50	5 - 100
7	HIMACHAL PRADESH	7	15,497.19	25,607.72	65.24	2	6,405.52	12,483.04	15 - 147
8	JAMMU AND KASHMIR	9	19,625.43	45,301.68	130.83	5	9,893.33	35,342.33	18 - 235
9	KARNATAKA	19	55,423.75	58,665.63	5.85	11	41,542.14	43,242.70	3 - 264
10	KERALA	9	30,871.86	34,193.65	10.76	5	15,319.19	16,962.71	8 - 33
11	MADHYA PRADESH	20	58,498.57	66,286.10	13.31	8	22,462.91	27,912.40	3 - 26
12	MAHARASHTRA	52	1,54,949.73	1,67,635.94	8.19	25	89,458.58	95,393.35	1 - 204
13	MANIPUR	1	4,454.17	12,524.00	181.17	1	4,454.17	12,524.00	108 - 108
14	MEGHALAYA	1	906.46	6,000.00	561.92	0	0.00	0.00	-
15	MIZORAM	1	2,393.47	5,021.45	109.80	1	2,393.47	5,021.45	96 - 96
16	NAGALAND	3	7,896.52	10,170.00	28.79	1	2,326.52	4,600.00	79 - 79
17	ODISHA	34	82,737.16	84,721.70	2.40	17	41,720.08	43,704.61	3 - 183
18	PUNJAB	3	3,627.54	4,765.00	31.36	0	0.00	0.00	-
19	RAJASTHAN	11	24,061.71	30,204.75	25.53	2	13,749.38	18,508.38	8 - 48
20	SIKKIM	1	1,339.48	4,084.69	204.95	0	0.00	0.00	-
21	TAMIL NADU	25	97,234.18	1,13,562.51	16.79	11	62,918.04	70,737.46	6 - 133
22	UTTAR PRADESH	42	1,11,806.06	1,16,702.16	4.38	15	38,372.65	42,417.85	2 - 40
23	WEST BENGAL	24	43,267.91	57,073.09	31.91	14	26,984.73	33,803.23	4 - 324
24	D & N HAVELI	1	6,086.08	5,842.31	-4.01	1	6,086.08	5,842.31	5 - 5
25	DELHI	7	50,481.91	58,224.75	15.34	2	2,613.73	3,394.52	17 - 31
26	CHHATISGARH	14	65,083.62	76,559.62	17.63	7	37,249.02	48,139.42	3 - 62
27	JHARKHAND	13	49,100.48	53,989.92	9.96	4	18,278.97	19,345.48	9 - 32
28	UTTARAKHAND	7	27,696.84	36,133.38	30.46	4	23,343.06	31,505.53	3 - 114
29	TELANGANA	5	18,567.06	20,644.30	11.19	3	13,026.06	13,303.46	7 - 156
30	MULTI STATE	59	2,87,449.36	3,90,572.54	35.88	25	76,583.36	1,15,760.93	7 - 252
Total		455	14,65,045.87	18,44,499.98	25.90	197	6,90,261.18	9,21,069.06	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-20

Extent of time overrun in projects with respect to latest schedule Rs.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	77,000.00	80,348.00	4.35	4	77,000.00	80,348.00	36 - 133
2	CIVIL AVIATION	2	3,850.00	3,850.00	0.00	1	2,467.00	2,467.00	6 - 6
3	COAL	16	67,189.78	69,715.09	3.76	2	8,135.46	8,135.46	31 - 48
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	-
5	STEEL	6	25,381.34	32,638.34	28.59	0	0.00	0.00	-
6	PETROLEUM	56	2,13,390.25	2,14,210.01	0.38	9	60,252.13	60,386.60	1 - 110
7	POWER	43	2,97,803.63	3,45,979.95	16.18	19	99,595.12	1,28,045.95	7 - 147
8	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	-
9	HEALTH AND FAMILY WELFARE	1	1,351.00	1,351.00	0.00	0	0.00	0.00	-
10	RAILWAYS	156	5,00,176.25	5,84,806.59	16.92	74	1,75,556.80	2,10,790.28	3 - 264
11	ROAD TRANSPORT AND HIGHWAYS	149	2,32,908.96	2,37,782.08	2.09	45	71,129.49	69,351.19	0 - 100
12	SHIPPING AND PORTS	1	5,369.18	5,369.18	0.00	0	0.00	0.00	-
13	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58 - 58
14	URBAN DEVELOPMENT	16	1,73,169.31	1,79,131.70	3.44	6	75,395.14	76,681.93	13 - 64
15	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	15 - 15
Total		455	16,30,279.91	18,44,499.98	13.14	162	5,93,016.18	7,16,419.28	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-21

Extent of cost overrun in projects with respect to latest schedule RS.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	77,000.00	80,348.00	4.35	1	3,492.00	6,840.00	95.88
2	CIVIL AVIATION	2	3,850.00	3,850.00	0.00	0	0.00	0.00	0.00
3	COAL	16	67,189.78	69,715.09	3.76	2	19,898.73	22,424.04	12.69
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
5	STEEL	6	25,381.34	32,638.34	28.59	1	15,525.00	23,140.00	49.05
6	PETROLEUM	56	2,13,390.25	2,14,210.01	0.38	7	13,807.27	16,382.59	18.65
7	POWER	43	2,97,803.63	3,45,979.95	16.18	20	1,25,822.18	1,74,515.55	38.70
8	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0.00
9	HEALTH AND FAMILY WELFARE	1	1,351.00	1,351.00	0.00	0	0.00	0.00	0.00
10	RAILWAYS	156	5,00,176.25	5,84,806.59	16.92	83	1,13,969.38	2,07,592.73	82.15
11	ROAD TRANSPORT AND HIGHWAYS	149	2,32,908.96	2,37,782.08	2.09	23	29,367.89	44,043.87	49.97
12	SHIPPING AND PORTS	1	5,369.18	5,369.18	0.00	0	0.00	0.00	0.00
13	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	84.97
14	URBAN DEVELOPMENT	16	1,73,169.31	1,79,131.70	3.44	5	26,335.97	32,298.36	22.64
15	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	447.22
Total		455	16,30,279.91	18,44,499.98	13.14	144	3,71,703.46	6,07,450.01	63.42

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-22

Extent of time & cost overrun in projects with respect to latest schedule Rs.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	77,000.00	80,348.00	4.35	1	3,492.00	6,840.00	133- 133
2	CIVIL AVIATION	2	3,850.00	3,850.00	0.00	0	0.00	0.00	0- 0
3	COAL	16	67,189.78	69,715.09	3.76	0	0.00	0.00	0- 0
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
5	STEEL	6	25,381.34	32,638.34	28.59	0	0.00	0.00	0- 0
6	PETROLEUM	56	2,13,390.25	2,14,210.01	0.38	1	2,915.00	3,049.47	110- 110
7	POWER	43	2,97,803.63	3,45,979.95	16.18	11	67,504.77	95,955.60	21- 147
8	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0- 0
9	HEALTH AND FAMILY WELFARE	1	1,351.00	1,351.00	0.00	0	0.00	0.00	0- 0
10	RAILWAYS	156	5,00,176.25	5,84,806.59	16.92	36	52,835.32	93,335.45	6- 252
11	ROAD TRANSPORT AND HIGHWAYS	149	2,32,908.96	2,37,782.08	2.09	11	10,655.43	14,009.63	2- 33
12	SHIPPING AND PORTS	1	5,369.18	5,369.18	0.00	0	0.00	0.00	0- 0
13	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58- 58
14	URBAN DEVELOPMENT	16	1,73,169.31	1,79,131.70	3.44	2	6,401.00	7,687.79	17- 29
15	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	15- 15
Total		455	16,30,279.91	18,44,499.98	13.14	64	1,67,288.56	3,01,090.81	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-23

Extent of time & cost overrun in projects with respect to original schedule Rs.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	48- 133
2	CIVIL AVIATION	2	3,850.00	3,850.00	0.00	0	0.00	0.00	0- 0
3	COAL	16	66,016.48	69,715.09	5.60	1	5,907.11	7,080.41	48- 48
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
5	STEEL	6	25,381.34	32,638.34	28.59	1	15,525.00	23,140.00	62- 62
6	PETROLEUM	56	2,06,905.35	2,14,210.01	3.53	10	27,585.94	32,737.08	1- 110
7	POWER	43	2,72,525.71	3,45,979.95	26.95	19	1,29,255.00	1,87,740.79	21- 147
8	HEAVY INDUSTRY	1	1,554.00	1,554.00	0.00	0	0.00	0.00	0- 0
9	HEALTH AND FAMILY WELFARE	1	1,351.00	1,351.00	0.00	0	0.00	0.00	0- 0
10	RAILWAYS	156	3,92,689.00	5,84,806.59	48.92	48	69,259.29	1,55,772.34	3- 324
11	ROAD TRANSPORT AND HIGHWAYS	149	2,19,449.56	2,37,782.08	8.35	15	17,085.22	23,201.79	1- 100
12	SHIPPING AND PORTS	1	4,200.00	5,369.18	27.84	0	0.00	0.00	0- 0
13	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58- 58
14	URBAN DEVELOPMENT	16	1,72,867.22	1,79,131.70	3.62	2	6,401.00	7,687.79	17- 29
15	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	15- 15
Total		455	14,65,045.87	18,44,499.98	25.90	101	3,21,774.60	5,58,072.07	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-24

State-Wise Position of Central Sector Projects costing Rs.1000 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	21	98,791.39	1,48,859.72	50.68	4	13,770.48	61,355.13	1 - 168
2	ARUNACHAL PRADESH	5	13,732.92	32,374.37	135.74	1	2,496.90	7,927.34	118 - 118
3	ASSAM	8	11,678.49	14,282.38	22.30	1	385.20	1,532.00	12 - 12
4	BIHAR	24	58,587.95	92,937.56	58.63	7	29,343.85	54,208.97	12 - 118
5	GUJARAT	18	46,707.74	53,208.72	13.92	2	12,288.74	17,890.23	12 - 54
6	HARYANA	11	16,490.84	18,350.34	11.28	1	1,108.00	2,967.50	100 - 100
7	HIMACHAL PRADESH	7	15,497.19	25,607.72	65.24	1	3,919.59	9,997.11	147 - 147
8	JAMMU AND KASHMIR	9	19,625.43	45,301.68	130.83	1	2,500.00	27,949.00	235 - 235
9	KARNATAKA	19	55,423.75	58,665.63	5.85	4	4,902.43	6,619.00	3 - 16
10	KERALA	9	30,871.86	34,193.65	10.76	4	12,006.19	13,673.75	15 - 33
11	MADHYA PRADESH	20	58,498.57	66,286.10	13.31	5	16,734.90	22,184.39	6 - 26
12	MAHARASHTRA	52	1,54,949.73	1,67,635.94	8.19	12	21,516.05	28,222.69	1 - 204
13	MANIPUR	1	4,454.17	12,524.00	181.17	1	4,454.17	12,524.00	108 - 108
14	MEGHALAYA	1	906.46	6,000.00	561.92	0	0.00	0.00	-
15	MIZORAM	1	2,393.47	5,021.45	109.80	1	2,393.47	5,021.45	96 - 96
16	NAGALAND	3	7,896.52	10,170.00	28.79	1	2,326.52	4,600.00	79 - 79
17	ODISHA	34	82,737.16	84,721.70	2.40	9	22,712.87	28,196.97	3 - 183
18	PUNJAB	3	3,627.54	4,765.00	31.36	0	0.00	0.00	-
19	RAJASTHAN	11	24,061.71	30,204.75	25.53	1	12,320.00	17,079.00	48 - 48
20	SIKKIM	1	1,339.48	4,084.69	204.95	0	0.00	0.00	-
21	TAMIL NADU	25	97,234.18	1,13,562.51	16.79	5	15,380.80	23,200.22	12 - 133
22	UTTAR PRADESH	42	1,11,806.06	1,16,702.16	4.38	4	13,450.10	17,668.28	5 - 40
23	WEST BENGAL	24	43,267.91	57,073.09	31.91	7	15,417.13	22,250.67	14 - 324
24	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	-
25	DELHI	7	50,481.91	58,224.75	15.34	1	1,219.21	2,000.00	17 - 17
26	CHHATISGARH	14	65,083.62	76,559.62	17.63	5	32,792.00	43,984.42	9 - 62
27	JHARKHAND	13	49,100.48	53,989.92	9.96	2	16,090.78	17,157.29	9 - 27
28	UTTARAKHAND	7	27,696.84	36,133.38	30.46	3	7,127.06	15,289.53	76 - 114
29	TELANGANA	5	18,567.06	20,644.30	11.19	1	1,266.60	1,544.00	36 - 36
30	MULTI STATE	59	2,87,449.36	3,90,572.54	35.88	17	53,851.56	93,029.13	8 - 178
Total		455	14,65,045.87	18,44,499.98	25.90	101	3,21,774.60	5,58,072.07	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-25

<u>List of projects completed/dropped/Frozen during current month Rs.150 Crore and above</u> (All Cost/ Expenditure in Rs. crore)							
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>PETROLEUM</u>						
1	URAN CHAKAN SHIKRAPUR LPG PIPELINE	12/2009	309.81	10/2014	723.40	08/2019	712.26
2	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT	09/2016	407.00	09/2019	407.00	09/2019	391.85

TABLE-26

List of projects added Rs.150 Crore and above					(September 2019)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	POWER					
1	KIRU HYDRO ELECTRIC PROJECT	3/2019	4,287.59	/	4,287.59	-

TABLE-27

Milestones (Cumulative due & achieved) Rs.150 Crore and above

Total	5440
Achieved up to month	2774

TABLE-28


<u>List of projects reporting additional delayed Rs.150 Crore and above</u>							(September 2019)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>COAL</u>						
1	SONEPUR BAZARI (COMB) OCP (8.0 MTY) ECL	1,055.05	1,055.05	03/2018	03/2020	10/2020	7
2	RG OC -III EXTENSION (PHASE -II) PROJECT SCCL	365.01	365.01	06/2015	12/2015	03/2020	51
	<u>STEEL</u>						
3	FORGED WHEEL PLANT RINL	1,682.85	1,682.85	09/2018	09/2019	10/2019	1
	<u>PETROLEUM</u>						
4	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY BPCL	554.00	554.00	02/2020	09/2019	10/2019	1
5	BS-VI PROJECT AT MATHURA REFINERY IOCL	666.64	666.64	09/2019	09/2019	01/2020	4
6	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY IOCL	2,934.40	2,934.40	09/2019	09/2019	01/2020	4
7	BS-VI PROJECT AT BONGAIGAON REFINERY IOCL	1,222.00	1,222.00	09/2019	09/2019	02/2020	5
8	BS-VI PROJECT AT GUJARAT REFINERY IOCL	3,380.00	3,380.00	09/2019	09/2019	03/2020	6
9	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA HPCL	249.26	249.26	06/2020	06/2020	09/2021	15
10	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE HPCL	161.50	161.50	06/2020	06/2020	09/2021	15
	<u>POWER</u>						
11	TAPOVAN-VISHNUGAD HEP (4X130MW) NTPC	2,978.48	5,867.38	03/2013	12/2020	01/2021	1
12	SYSTEM STRENGTHENING XIII OF SR GRID PGCIL	487.49	639.46	06/2014	09/2019	10/2019	1
13	TANDA TPP STAGE-II (2X660 MW) NTPC	9,188.98	9,188.98	07/2019	06/2020	07/2020	1
14	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) PGCIL	871.62	871.62	10/2017	09/2019	11/2019	2
15	DHUKWAN SMALL HYDRO PROJECT THDCIL	195.42	294.60	02/2014	10/2019	12/2019	2

List of projects reporting additional delayed Rs.150 Crore and above							(September 2019)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
16	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D PGCIL	3,519.59	3,519.59	05/2019	09/2019	12/2019	3
17	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) PGCIL	408.46	408.46	01/2019	09/2019	12/2019	3
18	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT PGCIL Central Sector Projects	175.64	175.64	09/2018	09/2019	12/2019	3
19	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY PGCIL Central Sector Projects	186.17	186.17	07/2019	09/2019	12/2019	3
20	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) PGCIL Central Sector Projects	445.89	445.89	02/2019	12/2019	03/2020	3
21	SUPPLEMENTARY TRANS. SYSTEM FOR UMSP AT BANASKANTHA (RADHANESDA) GUJARAT PGCIL	193.14	193.14	06/2019	09/2019	12/2019	3
22	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) PGCIL	235.53	235.53	06/2019	10/2019	03/2020	5
23	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P PGCIL	4,754.42	9,072.36	12/2018	12/2019	12/2020	12
	<u>RAILWAYS</u>						
24	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND SER	148.77	377.00	12/2016	11/2019	12/2019	1
25	KHURDA ROAD-BOLANGIR(NL)ECOR ECOR	2,923.13	3,791.66	03/2009	03/2024	06/2024	3
26	PALANPUR-SAMAKHAYALI (DL) RVNL	1,548.66	1,548.66	12/2021	12/2021	03/2022	3
27	BINA - KOTA DOUBLING WITH RE RVNL	1,485.85	1,485.85	12/2020	12/2020	03/2021	3
28	ALWAR-BANDIKUI DOUBLING NWR	242.09	410.00	02/2019	12/2019	05/2020	5
29	HANSDIHA-GODDA NL ER	542.18	693.80	03/2020	03/2020	03/2021	12
30	HOSPET-HUBLI-LONDA-VASCODAGAMA DL RVNL	2,127.00	2,900.00	03/2023	03/2023	03/2024	12
31	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE ECOR	701.61	810.02	11/2018	03/2021	03/2022	12
32	JHARSUGUDA-BILASPUR 4TH LINE SECR	1,973.00	1,973.66	03/2021	12/2021	12/2022	12


<u>List of projects reporting additional delayed Rs.150 Crore and above</u>							(September 2019)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
33	TALCHER-BIMALAGARH(NL)(ECOR) ECOR	810.78	1,928.07	06/2021	03/2023	06/2024	15
34	BANASPANI- JAKHPURA - DOUBLING RVNL	942.95	1,120.00	03/2019	03/2021	06/2022	15
35	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION RVNL	1,183.25	1,183.25	12/2020	03/2021	12/2022	21
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
36	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 NHAI	574.28	537.16	07/2018	09/2019	10/2019	1
37	FOUR LANING OF AURANGABAD - YEDISHI NHAI PPP (BOT)	1,871.34	1,871.34	01/2018	11/2019	12/2019	1
38	4-LANNING OF OTTANCHATRAM BYPASS NHAI Central Sector Projects	244.27	244.27	09/2017	11/2019	12/2019	1
39	NALBARI T BIJNI (AS-7) NHAI	208.00	230.00	04/2008	12/2019	03/2020	3
40	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T NHAI	804.97	804.97	06/2018	01/2020	04/2020	3
41	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD MORTH	319.28	319.28	08/2017	08/2019	03/2020	7
42	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 MORTH	376.25	376.25	08/2017	08/2019	03/2020	7
43	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION NHAI	1,069.65	1,069.65	N.A.	07/2019	03/2020	8
44	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 NHAI	1,008.96	1,008.96	N.A.	07/2020	03/2021	8
45	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A NHAI	2,136.97	2,136.97	12/2018	10/2019	07/2020	9
46	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) NHAI	239.68	235.90	03/2020	06/2019	03/2020	9
47	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU MORTH	372.68	372.68	02/2017	02/2019	12/2019	10
48	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 MORTH	290.15	290.15	05/2017	05/2019	03/2020	10
49	SONAPUR TO GUWAHTI (AS-3) NHAI	245.00	174.34	03/2008	09/2019	08/2020	11
50	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD MORTH	350.61	350.61	01/2017	07/2018	12/2019	17

<u>List of projects reporting additional delayed Rs.150 Crore and above</u>							(September 2019)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
51	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 MORTH	444.84	444.84	09/2016	09/2018	03/2020	18
52	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S NHAI	2,510.04	2,510.04	08/2019	08/2019	03/2021	19
53	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT MORTH	348.95	348.95	08/2016	08/2018	03/2020	19
54	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O MORTH	995.09	995.09	05/2016	05/2018	03/2020	22
55	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES PWD EPC	271.45	271.45	10/2015	10/2017	11/2019	25
56	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 MORTH	333.21	355.89	12/2015	12/2016	12/2019	36
	<u>TELECOMMUNICATIONS</u>						
57	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT BSNL Central Sector Projects	231.80	240.10	10/2018	09/2019	12/2019	3
	<u>URBAN DEVELOPMENT</u>						
58	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB CPWD	388.00	488.28	05/2017	09/2019	10/2019	1
59	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI CPWD	197.33	197.33	04/2019	06/2020	11/2020	5

Graphical Presentation of All Projects w.r.t. Original Schedule

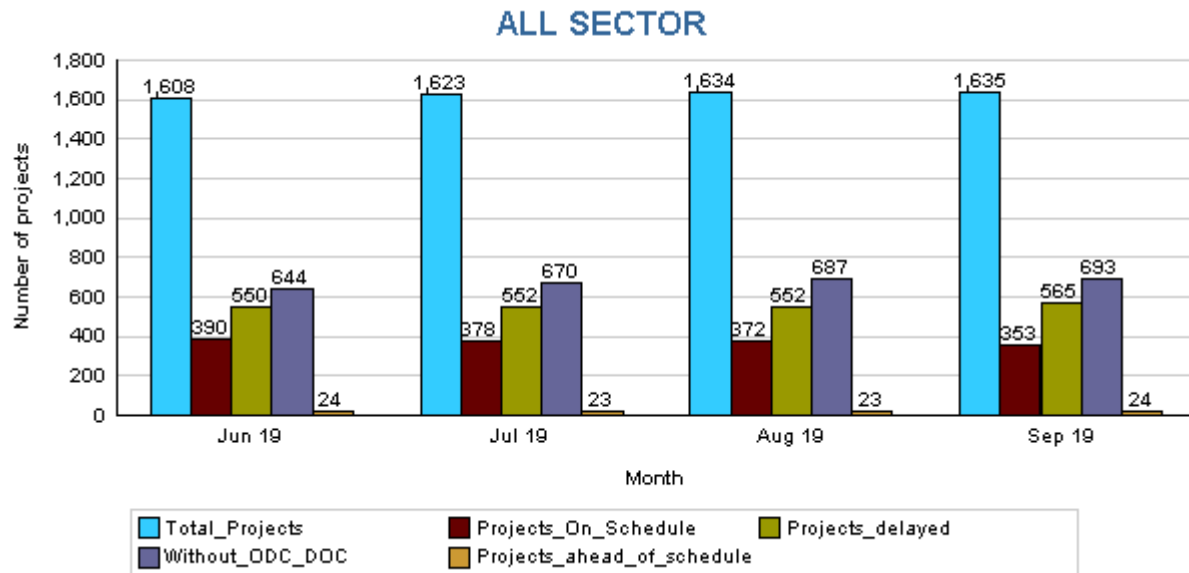


Break-up of 565 Delayed projects in September 2019

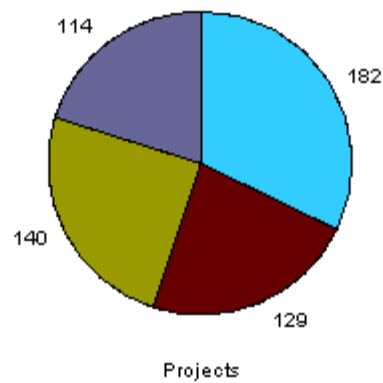


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

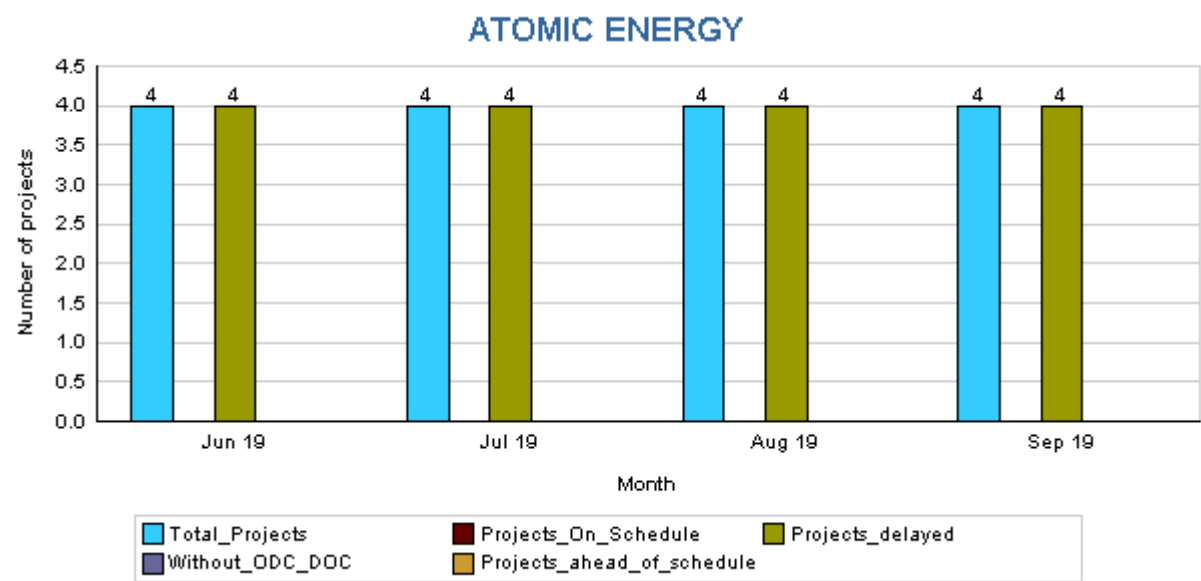


Break-up of 4 Delayed projects in September 2019

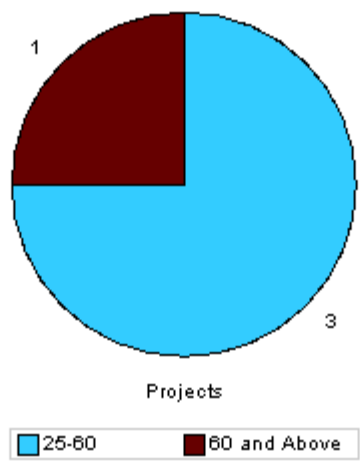


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

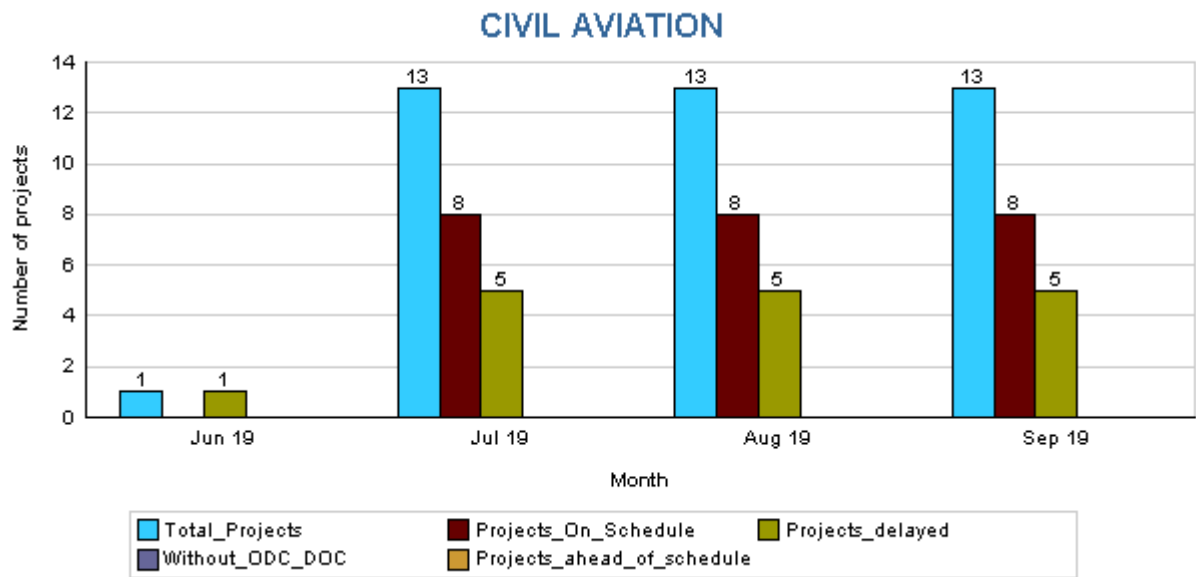


Break-up of 5 Delayed projects in September 2019

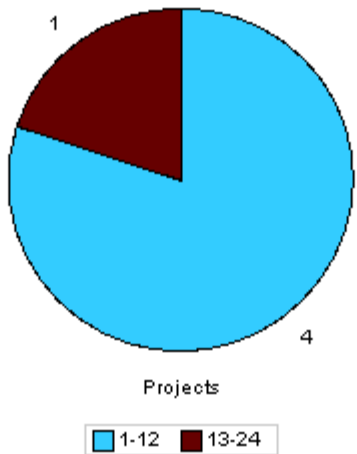


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

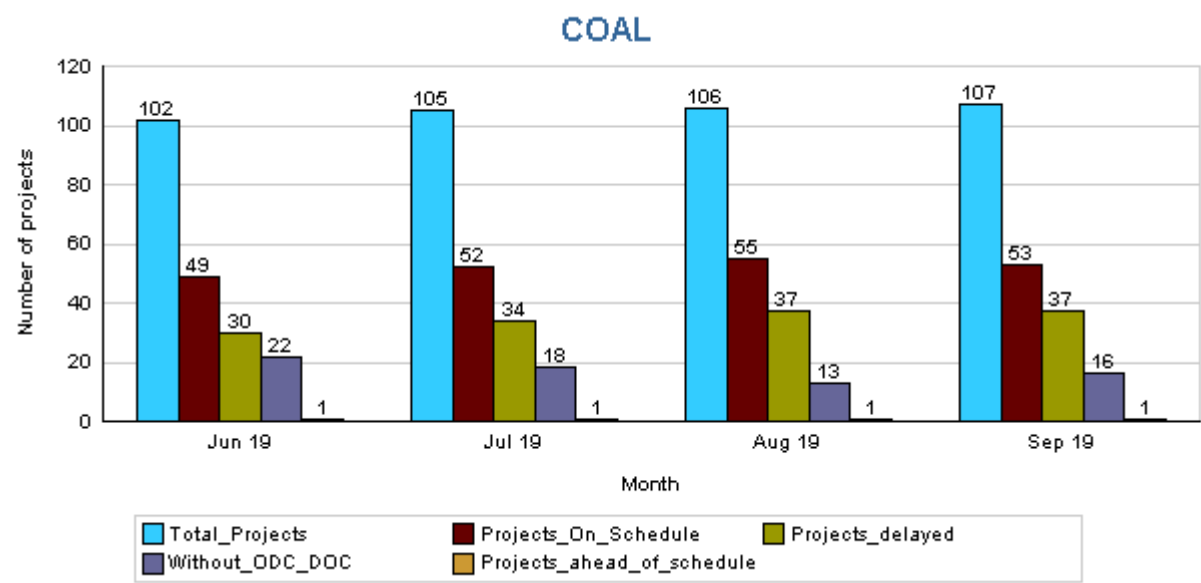


Break-up of 37 Delayed projects in September 2019

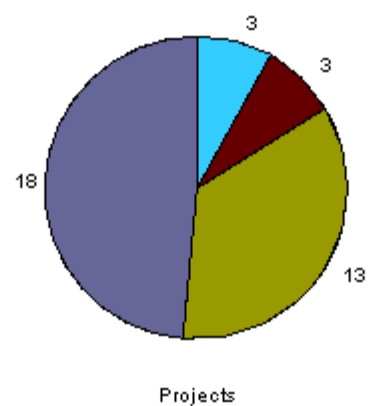


Delay in Months




Graphical Presentation of All Projects w.r.t. Original Schedule

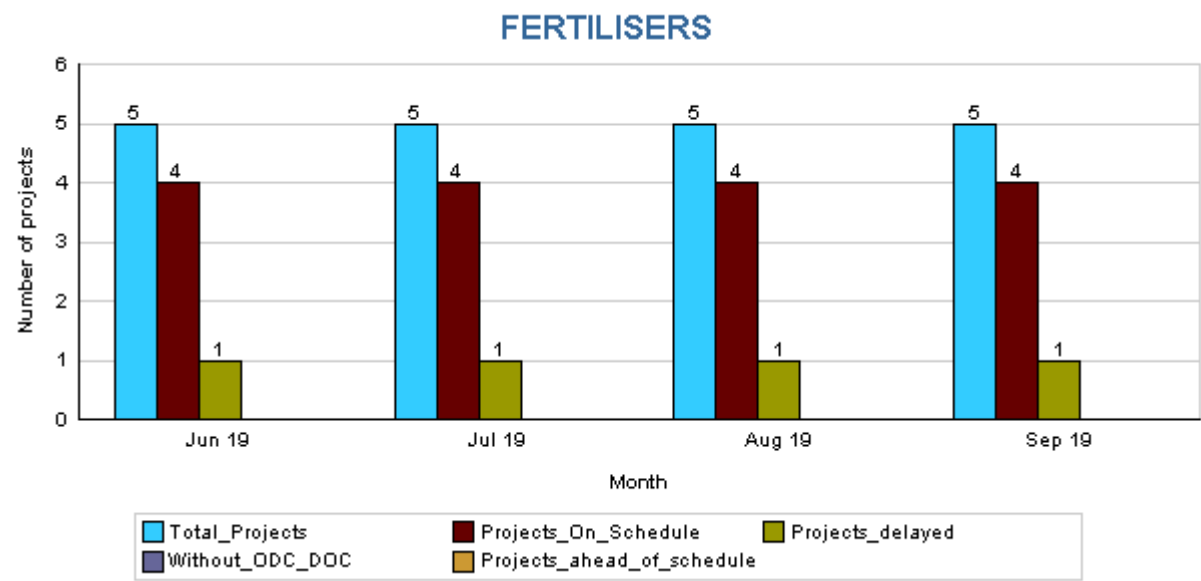


Break-up of 1 Delayed projects in September 2019



Delay in Months




Graphical Presentation of All Projects w.r.t. Original Schedule

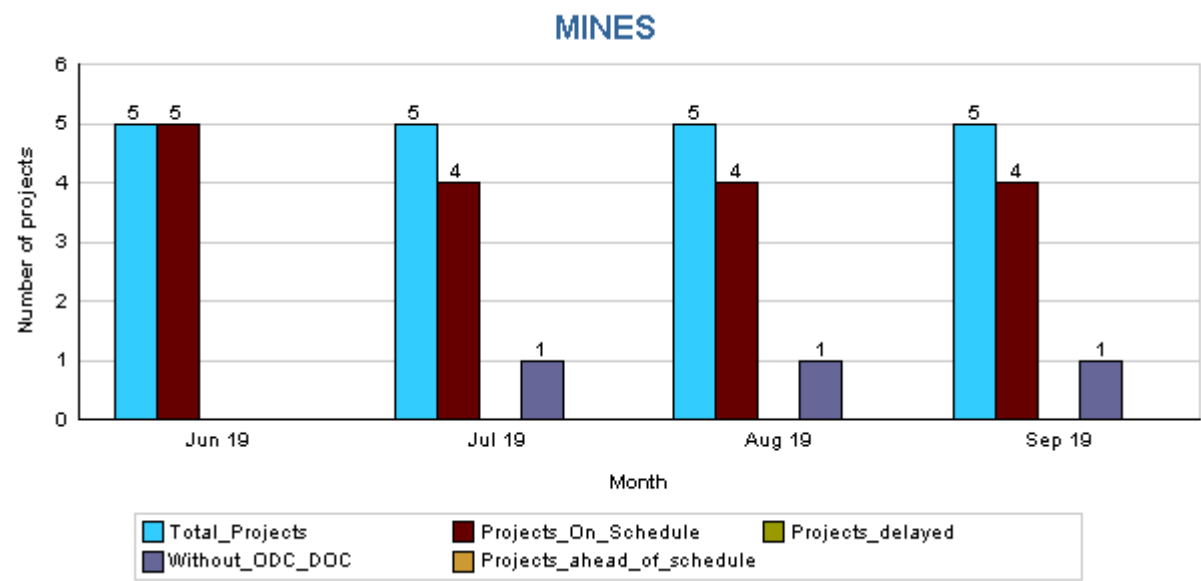


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

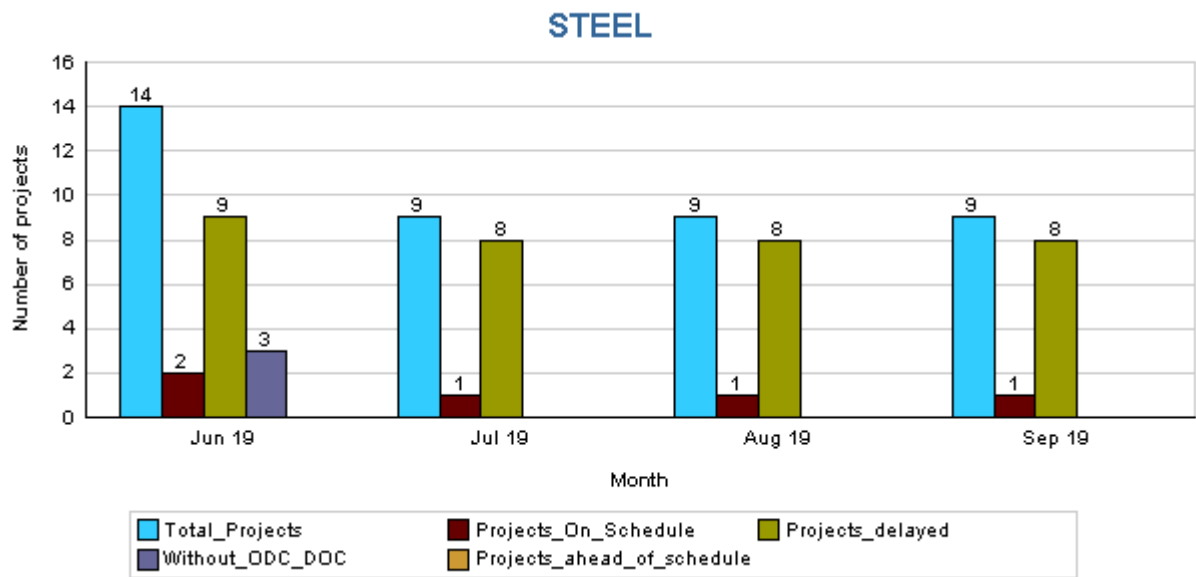


Break-up of 8 Delayed projects in September 2019

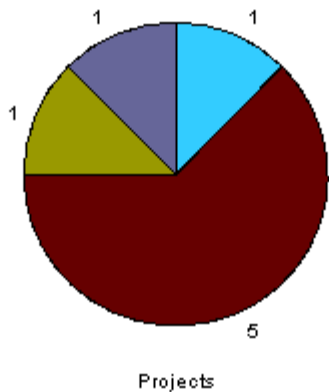


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

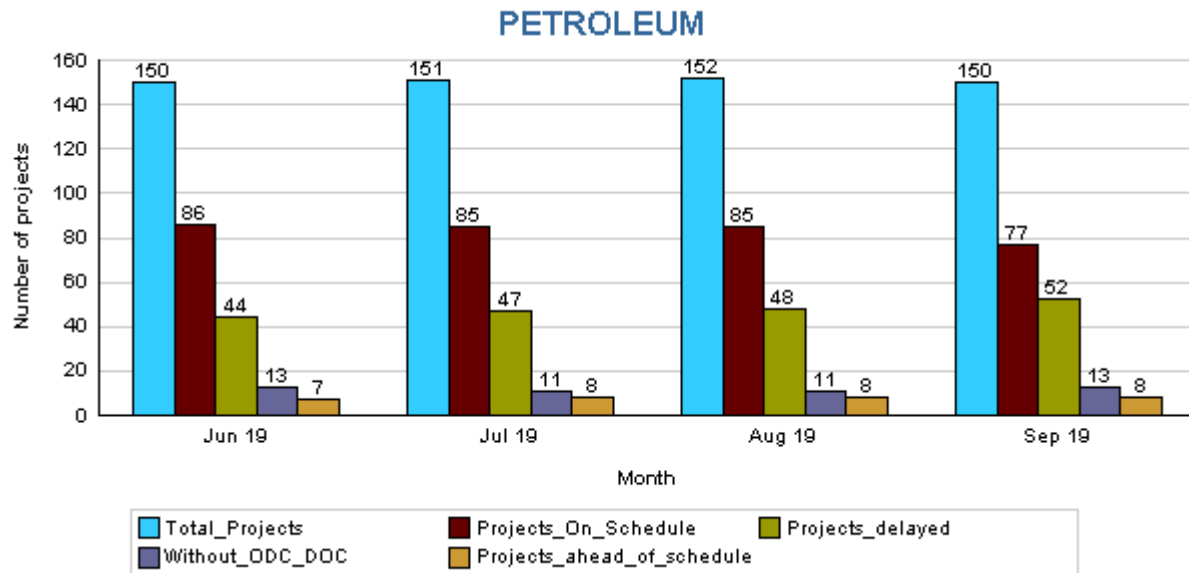


Break-up of 52 Delayed projects in September 2019

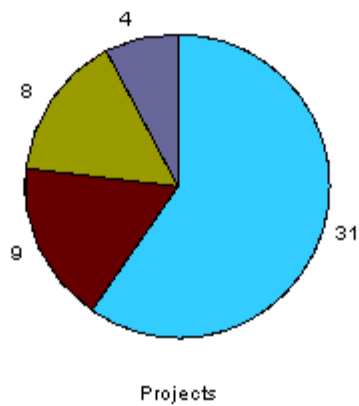


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

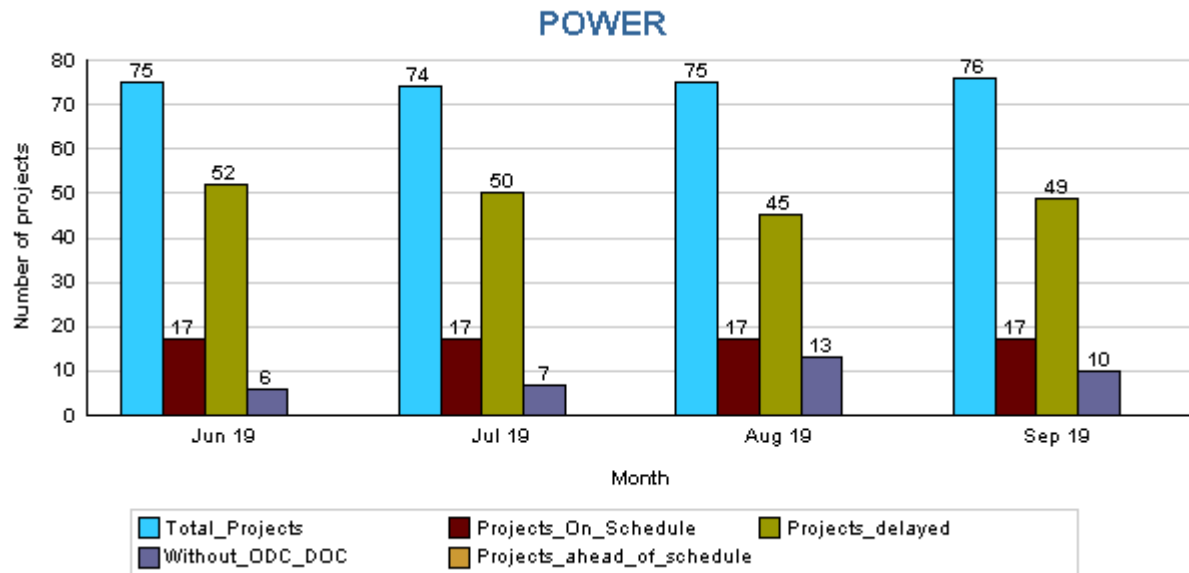


Break-up of 49 Delayed projects in September 2019

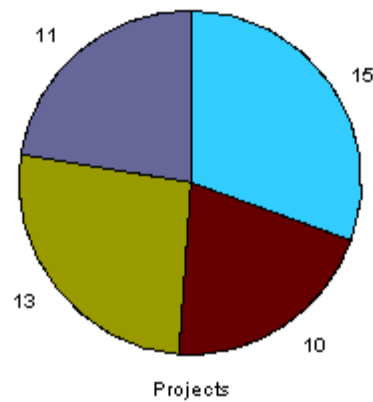

Delay in Months




Graphical Presentation of All Projects w.r.t. Original Schedule

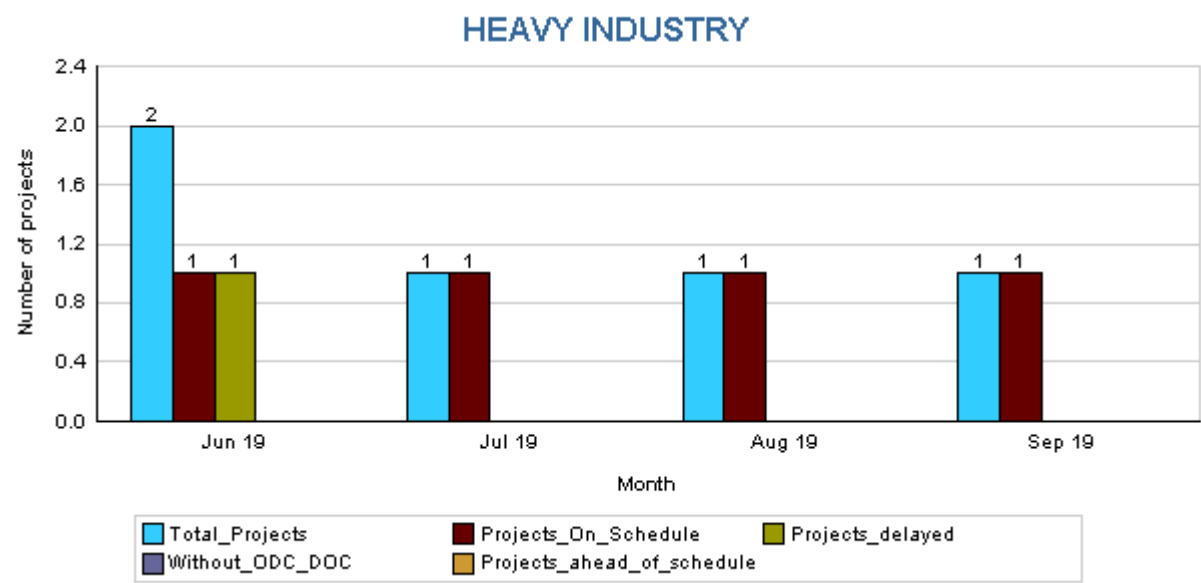


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

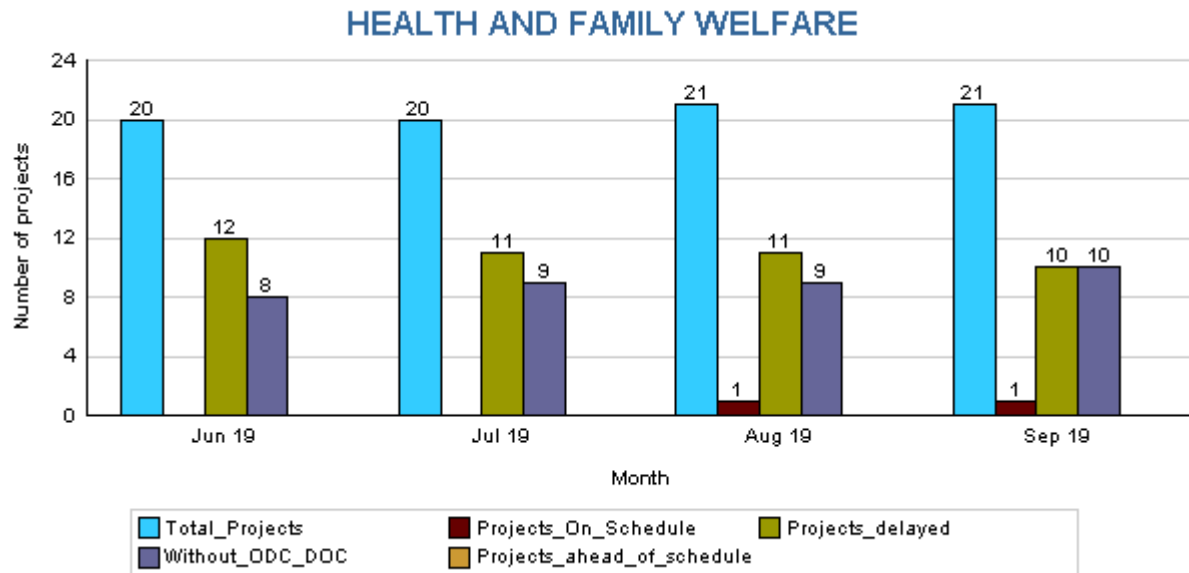


Break-up of 10 Delayed projects in September 2019

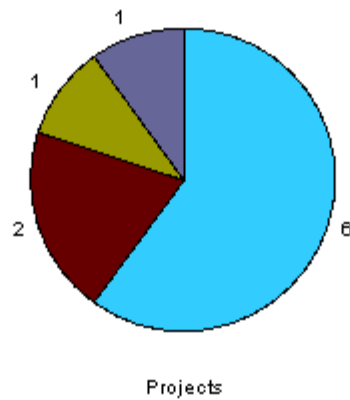


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

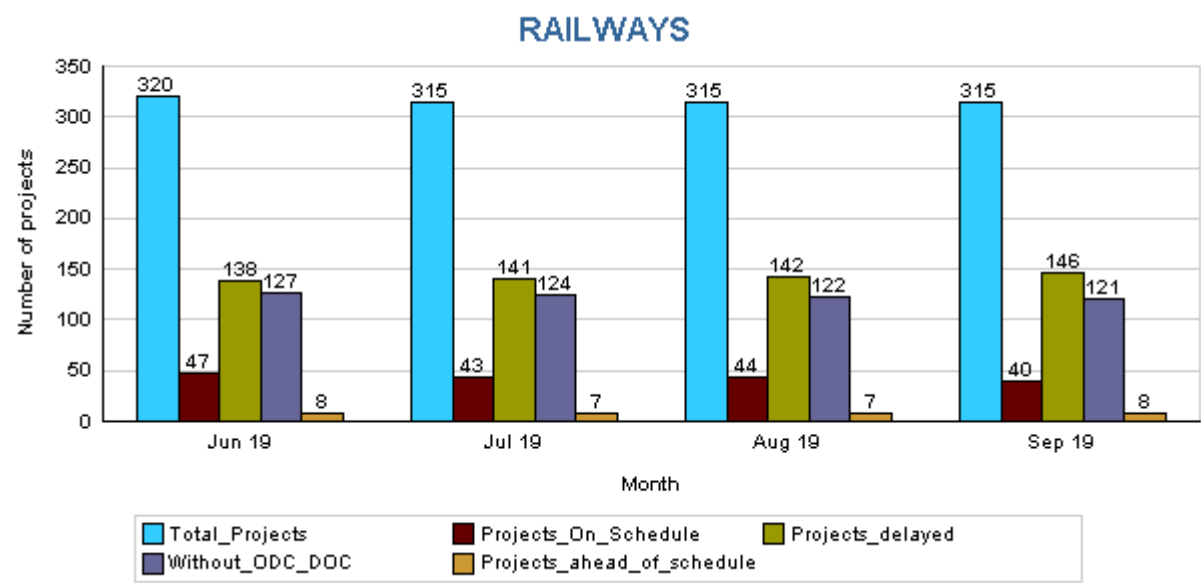


Break-up of 146 Delayed projects in September 2019

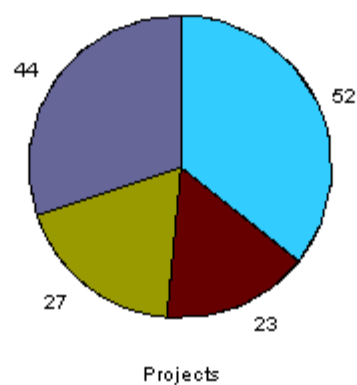


Delay in Months

Delay in Months	1-12	13-24	25-60	60 and Above

Graphical Presentation of All Projects w.r.t. Original Schedule

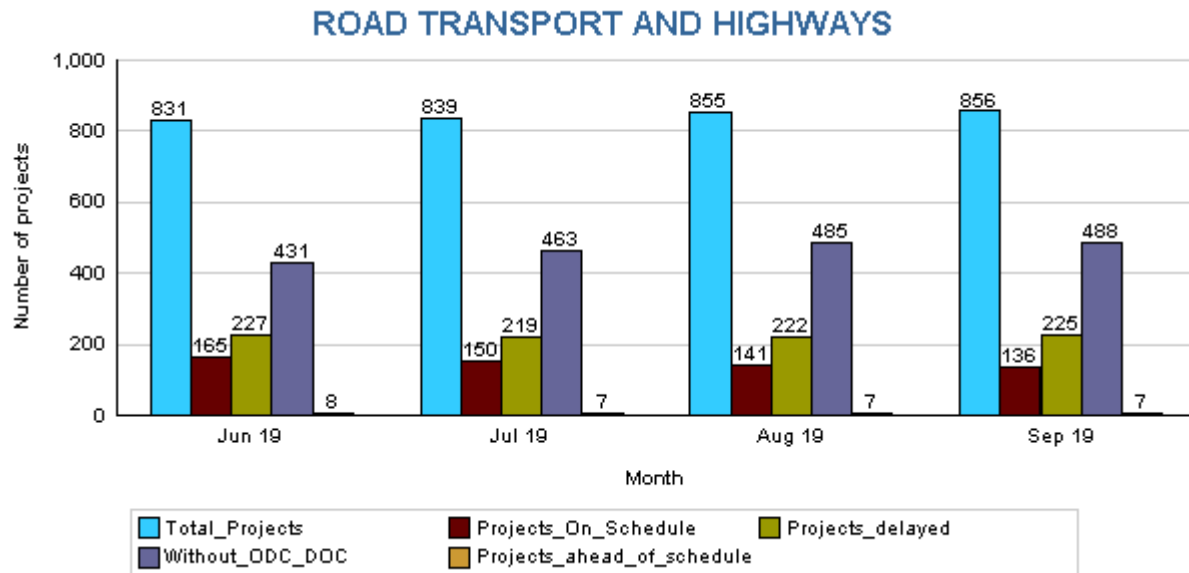


Break-up of 225 Delayed projects in September 2019

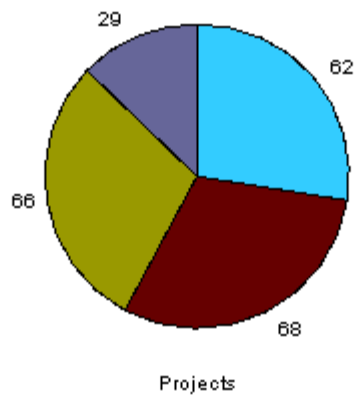


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

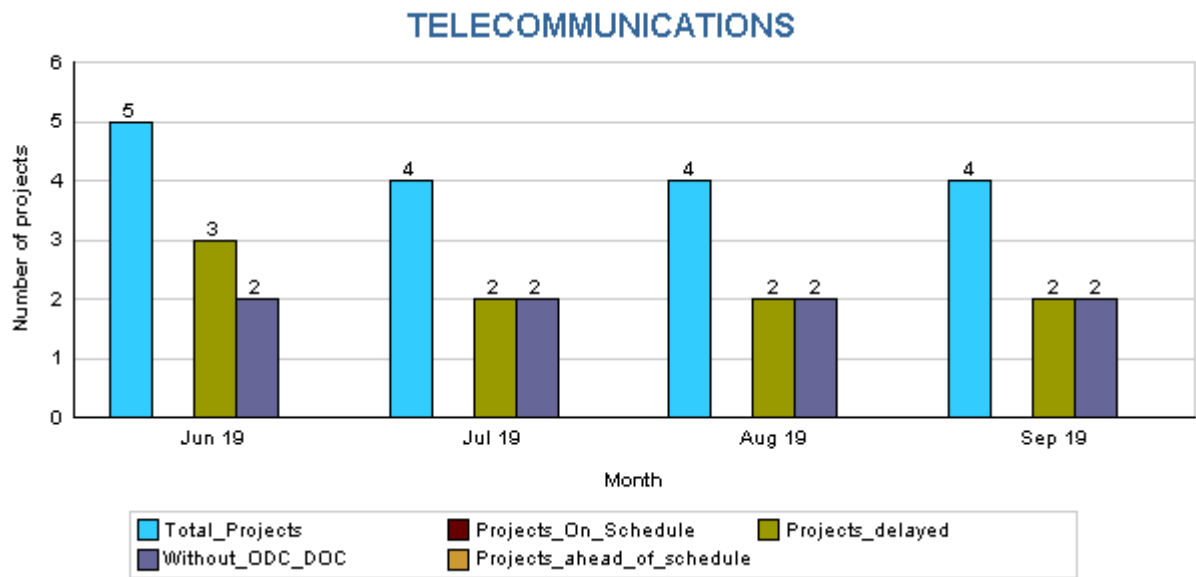


Break-up of 2 Delayed projects in September 2019

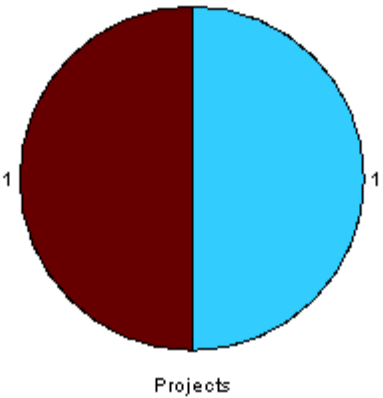

Delay in Months




Graphical Presentation of All Projects w.r.t. Original Schedule

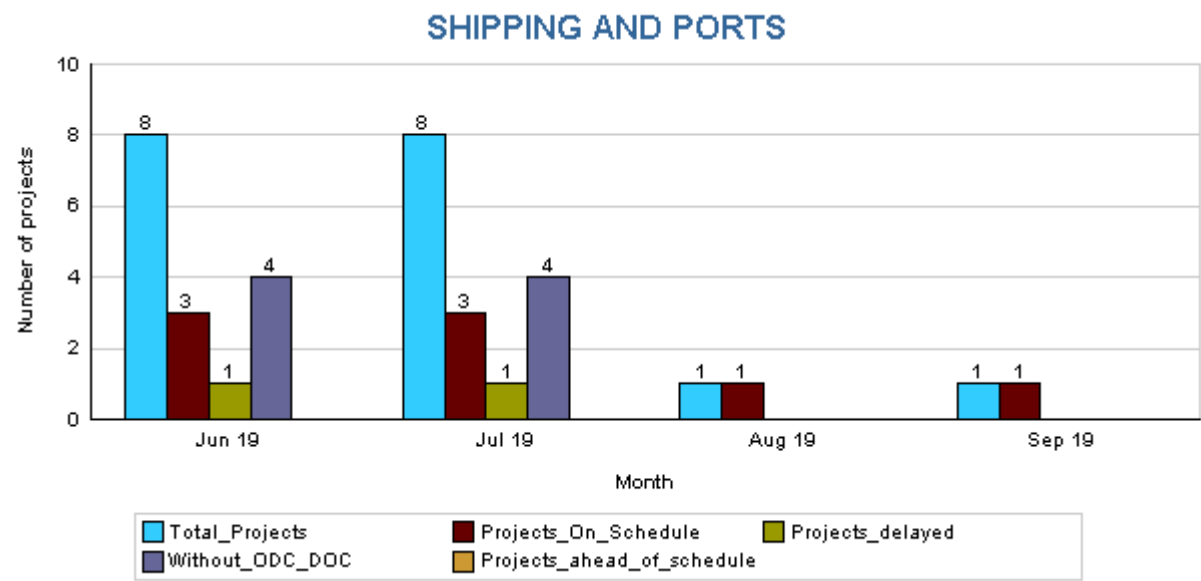


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

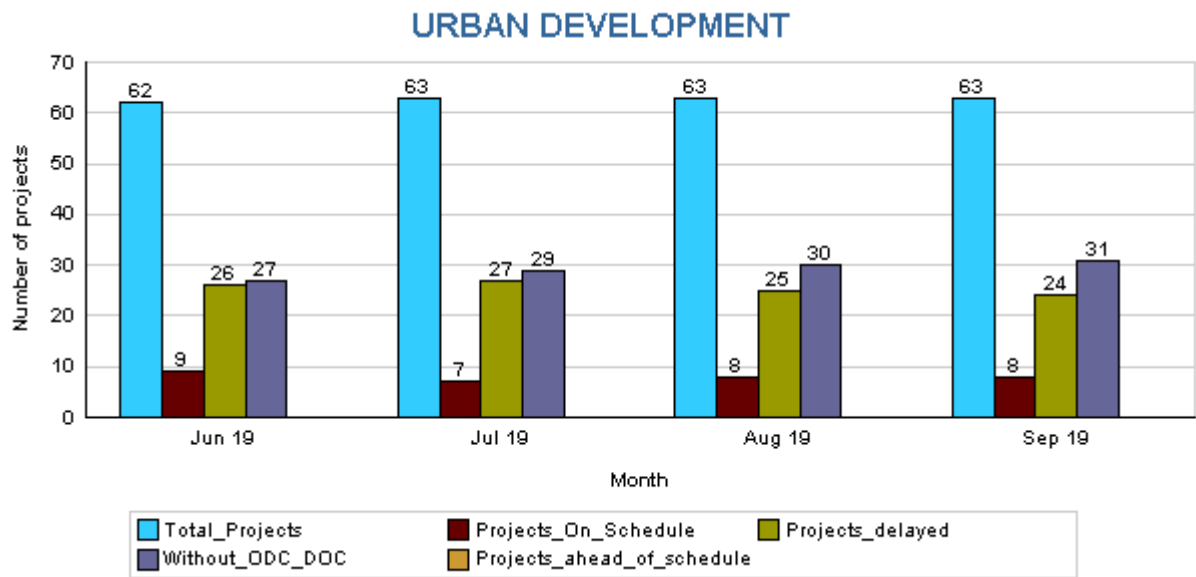


Break-up of 24 Delayed projects in September 2019

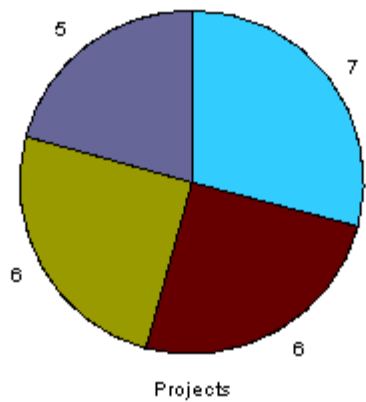


Delay in Months


Graphical Presentation of All Projects w.r.t. Original Schedule

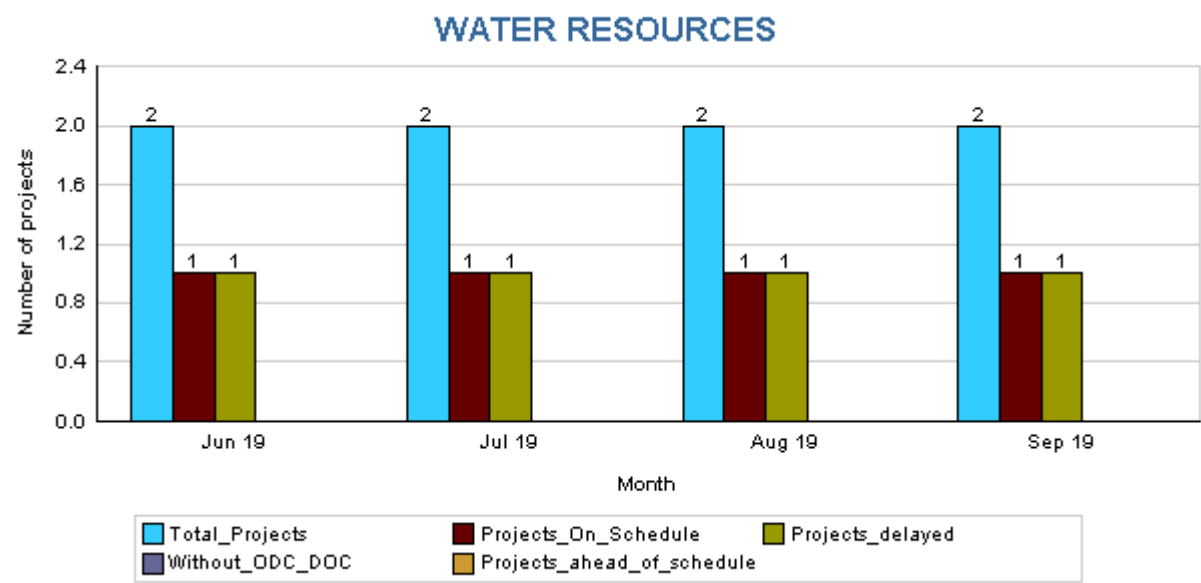


Break-up of 1 Delayed projects in September 2019



Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

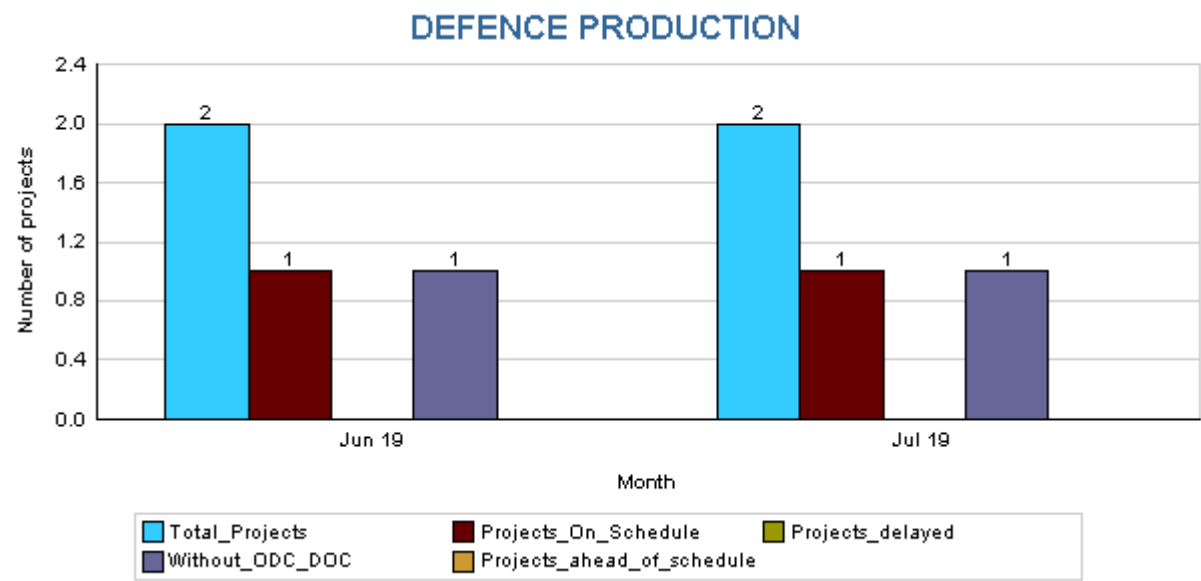

Delay in Months

TABLE-29

<u>Sector wise analysis of projects Rs.150 Crore and above</u>					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	67,120.00	770,00.00	80,348.00	47,051.38
CIVIL AVIATION	13	8,607.51	86,07.51	8,734.44	1,353.63
COAL	107	1,04,997.33	1,061,70.63	1,07,975.18	36,413.13
FERTILISERS	5	1,299.07	12,99.07	1,310.72	742.71
INFORMATION AND BROADCASTING	3	969.43	9,69.43	969.43	29.80
MINES	5	7,078.62	70,78.62	7,078.62	593.88
STEEL	9	26,228.23	262,28.23	33,485.23	23,460.75
PETROLEUM	150	2,45,939.08	2,527,07.26	2,53,886.39	93,345.17
POWER	76	2,85,786.68	3,110,64.60	3,59,673.67	2,19,075.70
HEAVY INDUSTRY	1	1,554.00	15,54.00	1,554.00	335.03
HEALTH AND FAMILY WELFARE	21	9,480.23	94,80.23	9,597.52	3,377.82
RAILWAYS	315	4,61,117.38	5,683,28.18	6,64,220.06	1,91,222.36
ROAD TRANSPORT AND HIGHWAYS	856	5,09,942.21	5,314,78.79	5,31,171.55	2,67,315.79
SHIPPING AND PORTS	1	4,200.00	53,69.18	5,369.18	1,400.95
TELECOMMUNICATIONS	4	16,095.23	161,03.53	27,333.53	9,135.56
URBAN DEVELOPMENT	63	1,86,663.06	1,872,05.75	1,93,294.88	85,310.09
WATER RESOURCES	2	10,384.61	103,84.61	55,782.44	16,450.19
Grand total	1635	19,47,462.67	21,21,029.62	23,41,784.84	9,96,613.94


Summary of projects in the Flash Report for the month of September, 2019

Project Implementation - Current Status:

Number of Projects in Previous Month	1634
Number of Projects completed/dropped/frozen in Current Month	2
Number of Projects elevated to the status of Major project during the current month	2
Number of Projects Added in Current Month	1
Number of Projects in Current Month	1635

Brief Analysis

Project Status with respect to Original Schedule: Out of 1635 projects, 24 projects are ahead of schedule, 353 projects are on schedule 565 projects are delayed. 517 projects do not have fixed dates of commissioning. 176 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

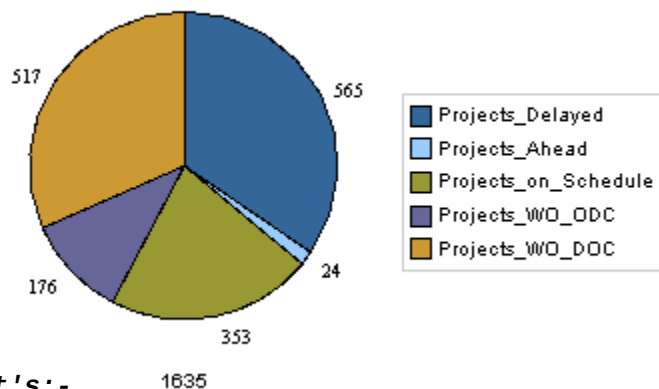


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1635 projects when sanctioned, was of the order of Rs. 1947711.22 crore but this was subsequently revised to Rs. 2342033.39 crore implying a cost overrun of 20.2%. The expenditure incurred on these projects till September, 2019 is Rs. 996613.94 crore, which is 42.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

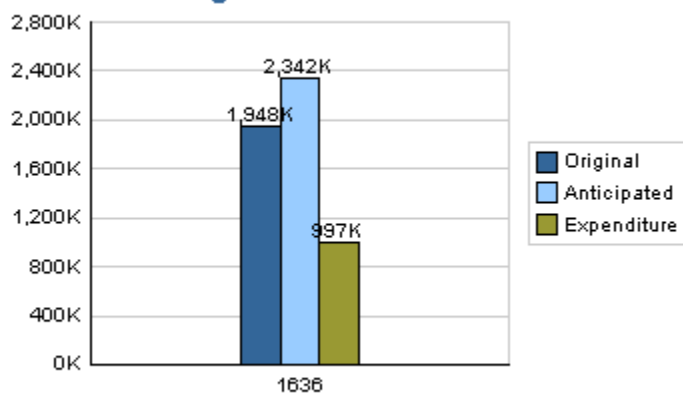

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	4

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed.

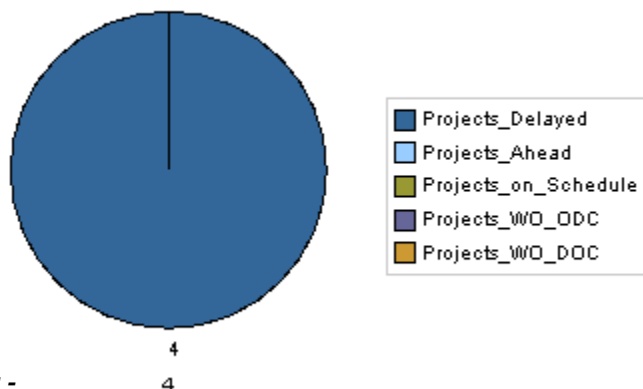

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 67120 crore but this was subsequently anticipated to Rs. 80348 crore implying a cost overrun of 19.7%. The expenditure incurred on these projects till September, 2019 is Rs. 47051.38 crore, which is 58.6% of the anticipated cost of the projects.

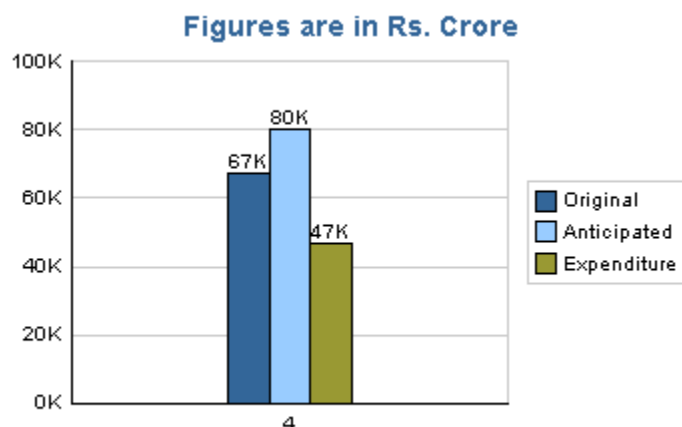

Sector wise current status of projects on the Flash Report


CIVIL AVIATION

Current Status:

Number of Projects	13
Number of Projects On Schedule	8
Number of Projects Delayed	5

Brief Analysis

Project Status with respect to Original Schedule: Out of 13 projects, 8 projects are on schedule 5 projects are delayed.

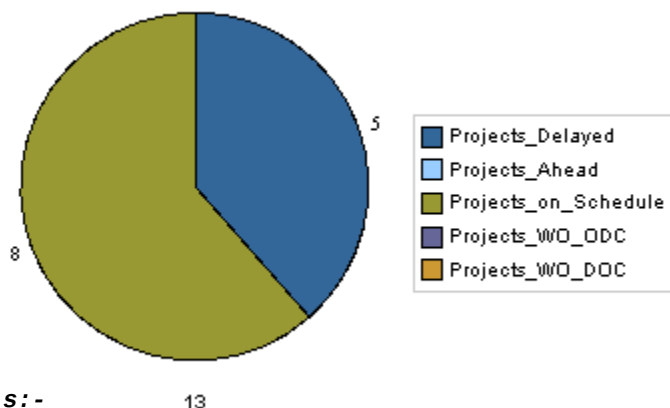


Total No Of Project's:-

13

Investment Scenario

Total original cost of implementation of 13 projects when sanctioned, was of the order of Rs. 8607.51 crore but this was subsequently anticipated to Rs. 8734.44 crore implying a cost overrun of 1.5%. The expenditure incurred on these projects till September, 2019 is Rs. 1353.63 crore, which is 15.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

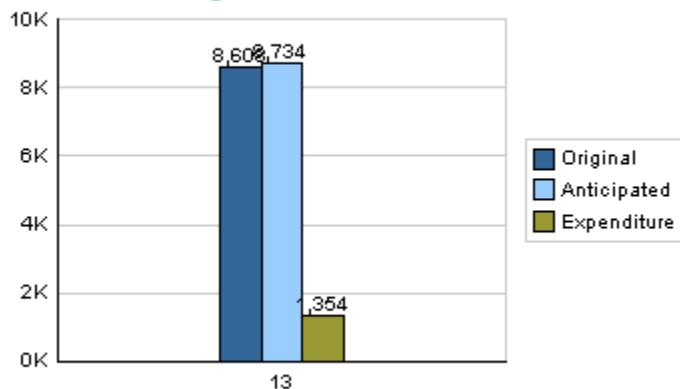

Sector wise current status of projects on the Flash Report


COAL

Current Status:

Number of Projects	107
Number of Projects On Schedule	53
Number of Projects Delayed	37
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	3
Number of Projects Without Date Of Commissioning	13

Brief Analysis

Project Status with respect to Original Schedule: Out of 107 projects, 1 project is ahead of schedule, 53 projects are on schedule 37 projects are delayed. 13 projects do not have fixed dates of commissioning. 3 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

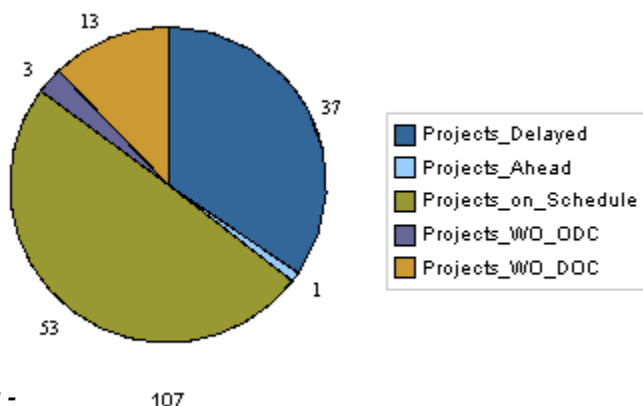


Total No Of Project's:-

107

Investment Scenario

Total original cost of implementation of 107 projects when sanctioned, was of the order of Rs. 104997.33 crore but this was subsequently anticipated to Rs. 107975.18 crore implying a cost overrun of 2.8%. The expenditure incurred on these projects till September, 2019 is Rs. 36413.13 crore, which is 33.7% of the anticipated cost of the projects.

Figures are in Rs. Crore

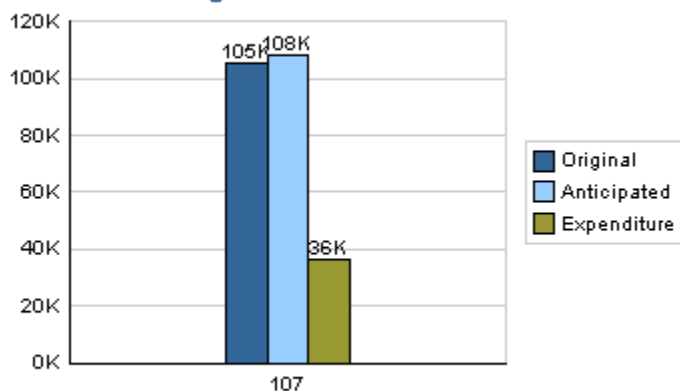

Sector wise current status of projects on the Flash Report


FERTILISERS

Current Status:

Number of Projects	5
Number of Projects On Schedule	4
Number of Projects Delayed	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 5 projects, 4 projects are on schedule 1 project is delayed.

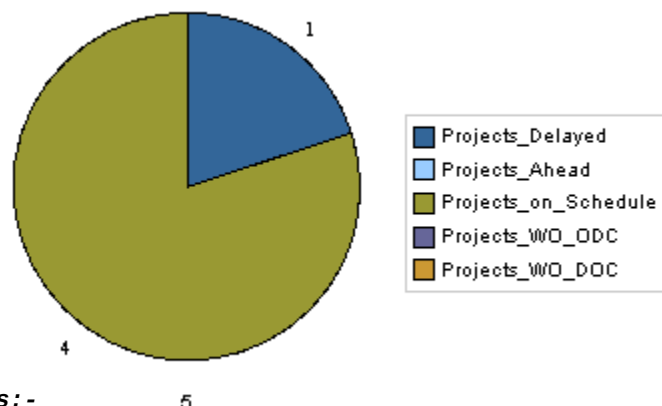


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 1299.07 crore but this was subsequently anticipated to Rs. 1310.72 crore implying a cost overrun of .9%. The expenditure incurred on these projects till September, 2019 is Rs. 742.71 crore, which is 56.7% of the anticipated cost of the projects.

Figures are in Rs. Crore

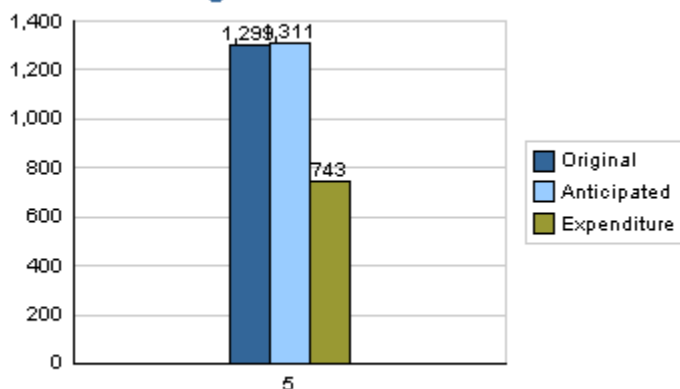

Sector wise current status of projects on the Flash Report

MINES


Current Status:

Number of Projects	5
Number of Projects On Schedule	4

Number of Projects Without Date Of Commissioning	1
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 5 projects, 4 projects are on schedule 1 project does not have fixed dates of commissioning.

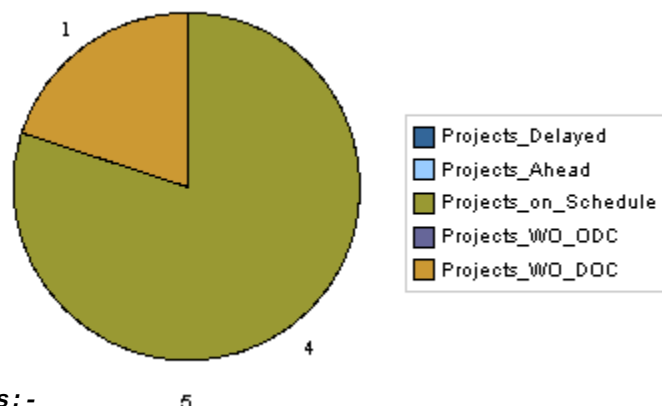


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 7078.62 crore but this was subsequently anticipated to Rs. 7078.62 crore. The expenditure incurred on these projects till September, 2019 is Rs. 593.88 crore, which is 8.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

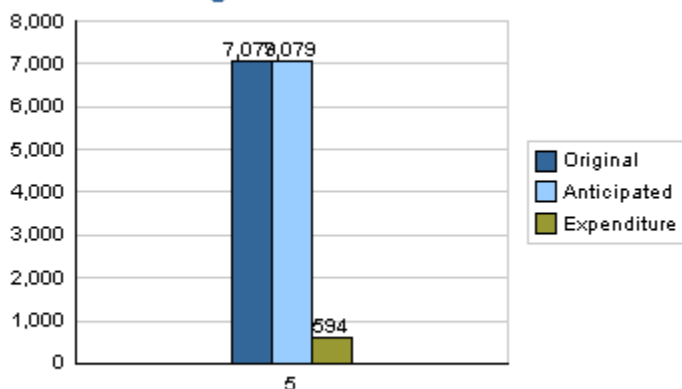

Sector wise current status of projects on the Flash Report


STEEL

Current Status:

Number of Projects	9
Number of Projects On Schedule	1
Number of Projects Delayed	8

Brief Analysis

Project Status with respect to Original Schedule: Out of 9 projects, 1 project is on schedule 8 projects are delayed.

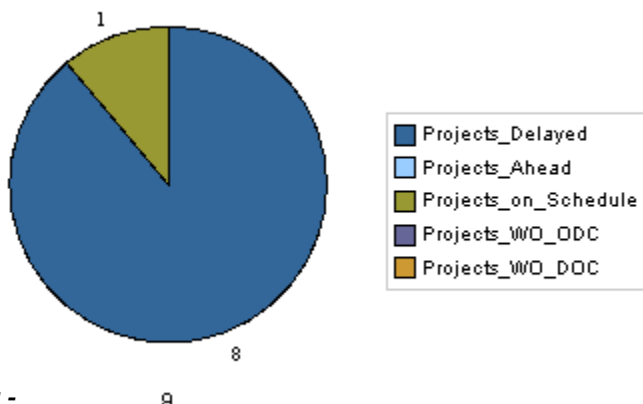


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 9 projects when sanctioned, was of the order of Rs. 26228.23 crore but this was subsequently anticipated to Rs. 33485.23 crore implying a cost overrun of 27.7%. The expenditure incurred on these projects till September, 2019 is Rs. 23460.75 crore, which is 70.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

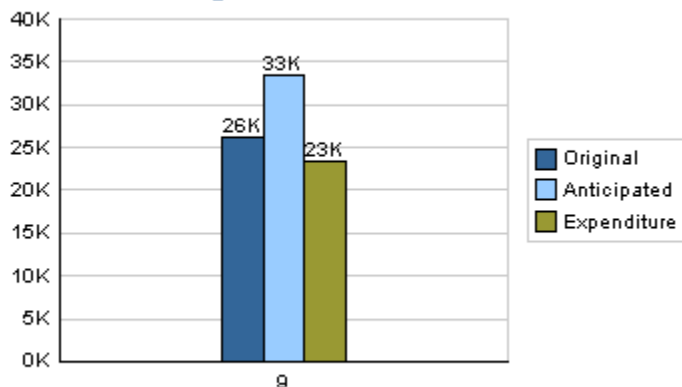

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	151
Number of Projects On Schedule	77
Number of Projects Delayed	52
Number of Projects Ahead	8
Number of Projects Without Original Date of Commissioning	2
Number of Projects Without Date Of Commissioning	11

Brief Analysis

Project Status with respect to Original Schedule: Out of 150 projects, 8 projects are ahead of schedule, 77 projects are on schedule 52 projects are delayed. 11 projects do not have fixed dates of commissioning. 2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

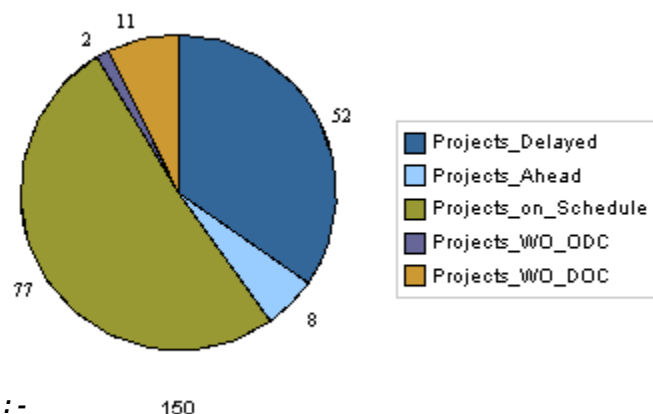


Total No Of Project's:-

150

Investment Scenario

Total original cost of implementation of 151 projects when sanctioned, was of the order of Rs. 246187.63 crore but this was subsequently anticipated to Rs. 254134.94 crore implying a cost overrun of 3.2%. The expenditure incurred on these projects till September, 2019 is Rs. 93345.17 crore, which is 36.7% of the anticipated cost of the projects.

Figures are in Rs. Crore

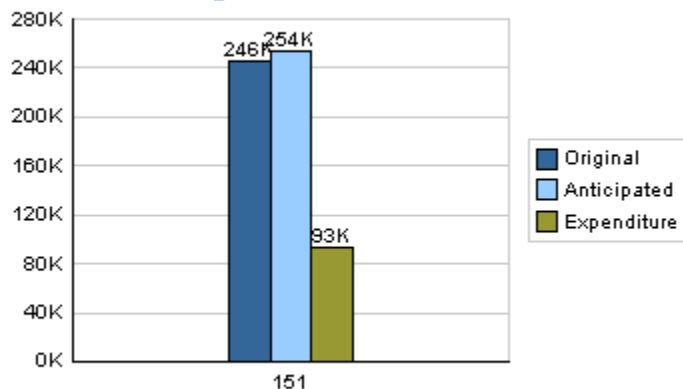

Sector wise current status of projects on the Flash Report

POWER


Current Status:

Number of Projects	76
Number of Projects On Schedule	17
Number of Projects Delayed	49

Number of Projects Without Date Of Commissioning 10

Brief Analysis

Project Status with respect to Original Schedule: Out of 76 projects, 17 projects are on schedule 49 projects are delayed. 10 projects do not have fixed dates of commissioning.

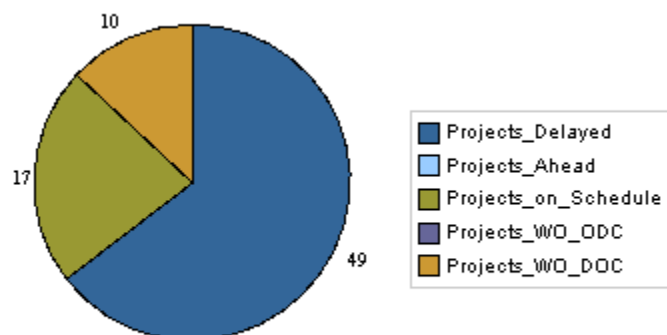


Total No Of Project's:-

76

Investment Scenario

Total original cost of implementation of 76 projects when sanctioned, was of the order of Rs. 285786.68 crore but this was subsequently anticipated to Rs. 359673.67 crore implying a cost overrun of 25.9%. The expenditure incurred on these projects till September, 2019 is Rs. 219075.7 crore, which is 60.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

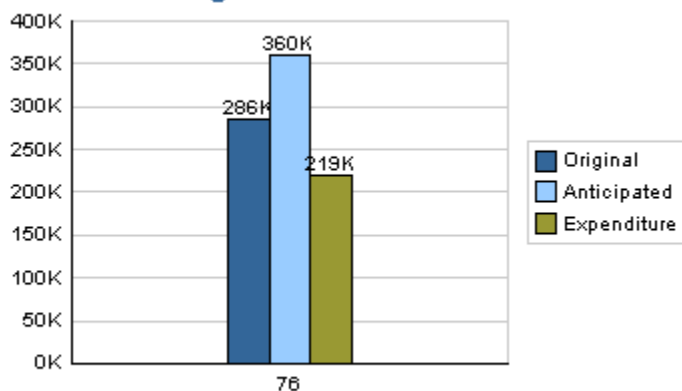

Sector wise current status of projects on the Flash Report


HEAVY INDUSTRY

Current Status:

Number of Projects	1
Number of Projects On Schedule	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 1 project, 1 project is on schedule




Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 1554 crore but this was subsequently anticipated to Rs. 1554 crore. The expenditure incurred on these projects till September, 2019 is Rs. 335.03 crore, which is 21.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

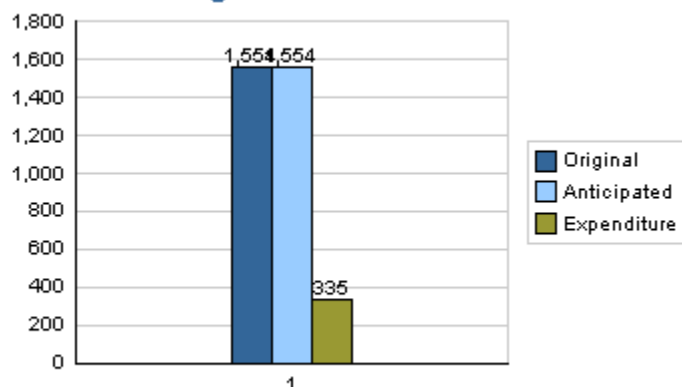

Sector wise current status of projects on the Flash Report

HEALTH AND FAMILY WELFARE


Current Status:

Number of Projects	21
Number of Projects On Schedule	1
Number of Projects Delayed	10

Number of Projects Without Original Date of Commissioning	6
Number of Projects Without Date Of Commissioning	4

Brief Analysis

Project Status with respect to Original Schedule: Out of 21 projects, 1 project is on schedule 10 projects are delayed. 4 projects do not have fixed dates of commissioning. 6 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

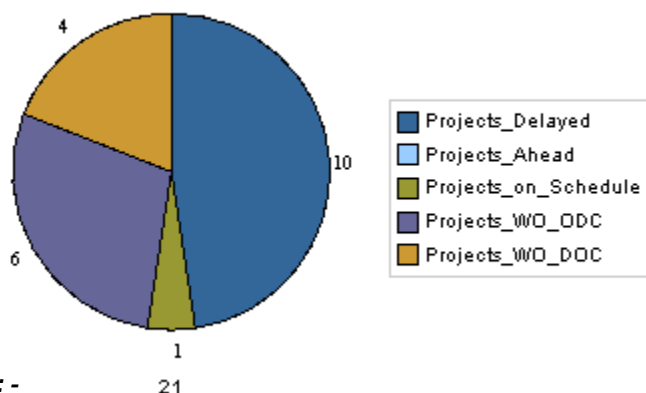


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 21 projects when sanctioned, was of the order of Rs. 9480.23 crore but this was subsequently anticipated to Rs. 9597.52 crore implying a cost overrun of 1.2%. The expenditure incurred on these projects till September, 2019 is Rs. 3377.82 crore, which is 35.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

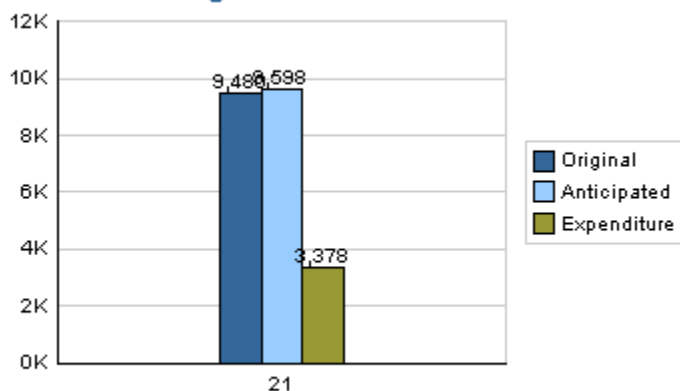

Sector wise current status of projects on the Flash Report

RAILWAYS


Current Status:

Number of Projects	315
Number of Projects On Schedule	40
Number of Projects Delayed	146
Number of Projects Ahead	8
Number of Projects Without Original Date of Commissioning	59
Number of Projects Without Date Of Commissioning	62

Brief Analysis

Project Status with respect to Original Schedule: Out of 315 projects, 8 projects are ahead of schedule, 40 projects are on schedule 146 projects are delayed. 62 projects do not have fixed dates of commissioning. 59 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.


Total No Of Project's:-

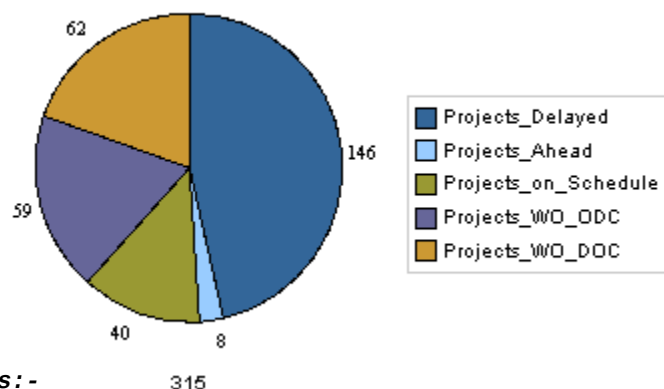

Investment Scenario

Total original cost of implementation of 315 projects when sanctioned, was of the order of Rs. 461117.38 crore but this was subsequently anticipated to Rs. 664220.06 crore implying a cost overrun of 44%. The expenditure incurred on these projects till September, 2019 is Rs. 191222.36 crore, which is 28.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

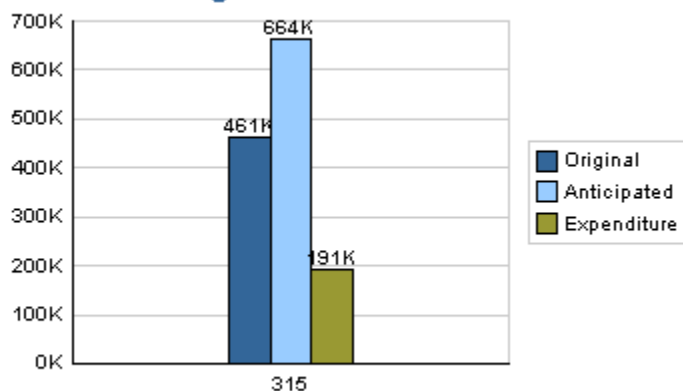

Sector wise current status of projects on the Flash Report

ROAD TRANSPORT AND HIGHWAYS


Current Status:

Number of Projects	856
Number of Projects On Schedule	136
Number of Projects Delayed	225
Number of Projects Ahead	7
Number of Projects Without Original Date of Commissioning	103
Number of Projects Without Date Of Commissioning	385

Brief Analysis

Project Status with respect to Original Schedule: Out of 856 projects, 7 projects are ahead of schedule, 136 projects are on schedule 225 projects are delayed. 385 projects do not have fixed dates of commissioning. 103 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.


Total No Of Project's:-

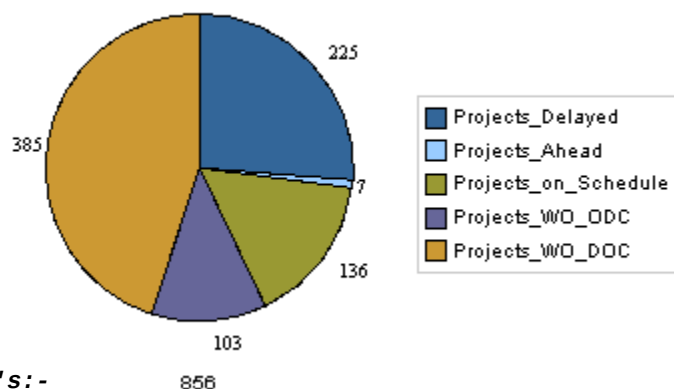

Investment Scenario

Total original cost of implementation of 856 projects when sanctioned, was of the order of Rs. 509942.21 crore but this was subsequently anticipated to Rs. 531171.55 crore implying a cost overrun of 4.2%. The expenditure incurred on these projects till September, 2019 is Rs. 267315.79 crore, which is 50.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

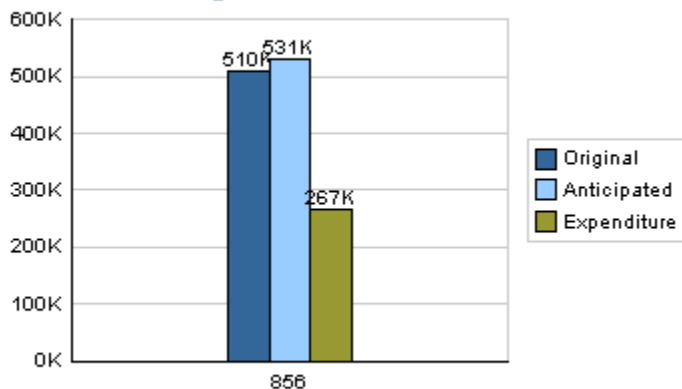

Sector wise current status of projects on the Flash Report


SHIPPING AND PORTS

Current Status:

Number of Projects	1
Number of Projects On Schedule	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 1 project, 1 project is on schedule




Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 4200 crore but this was subsequently anticipated to Rs. 5369.18 crore implying a cost overrun of 27.8%. The expenditure incurred on these projects till September, 2019 is Rs. 1400.95 crore, which is 26.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

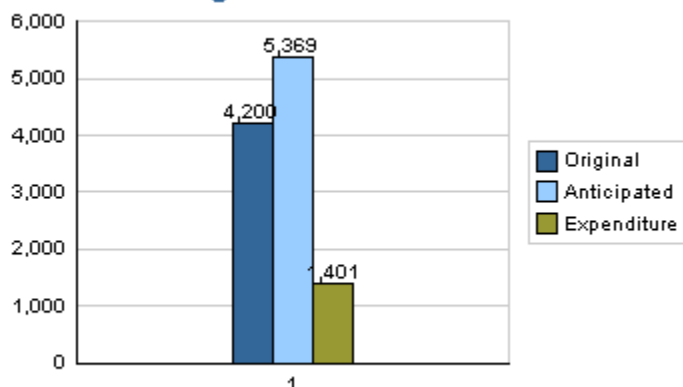

Sector wise current status of projects on the Flash Report

TELECOMMUNICATIONS

Current Status:


Number of Projects 4

Number of Projects Delayed 2

Number of Projects Without Date Of Commissioning 2

Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 2 projects are delayed. 2 projects do not have fixed dates of commissioning.

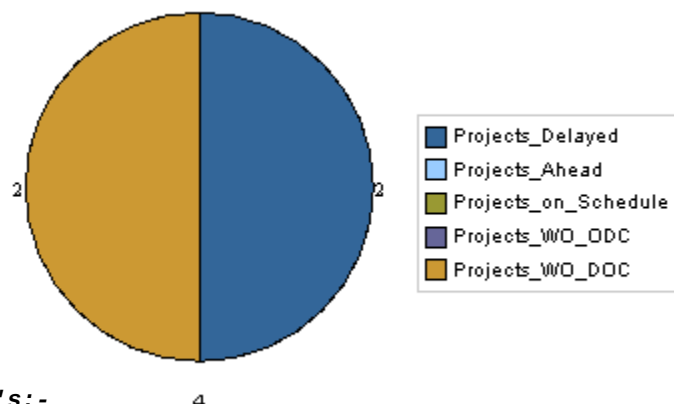


Total No Of Project's:-

4

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 16095.23 crore but this was subsequently anticipated to Rs. 27333.53 crore implying a cost overrun of 69.8%. The expenditure incurred on these projects till September, 2019 is Rs. 9135.56 crore, which is 33.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

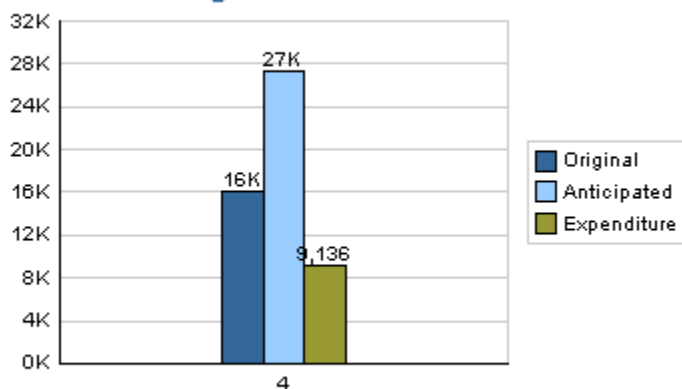

Sector wise current status of projects on the Flash Report

URBAN DEVELOPMENT


Current Status:

Number of Projects	63
Number of Projects On Schedule	8
Number of Projects Delayed	24

Number of Projects Without Original Date of Commissioning	3
Number of Projects Without Date Of Commissioning	28

Brief Analysis

Project Status with respect to Original Schedule: Out of 63 projects, 8 projects are on schedule 24 projects are delayed. 28 projects do not have fixed dates of commissioning. 3 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

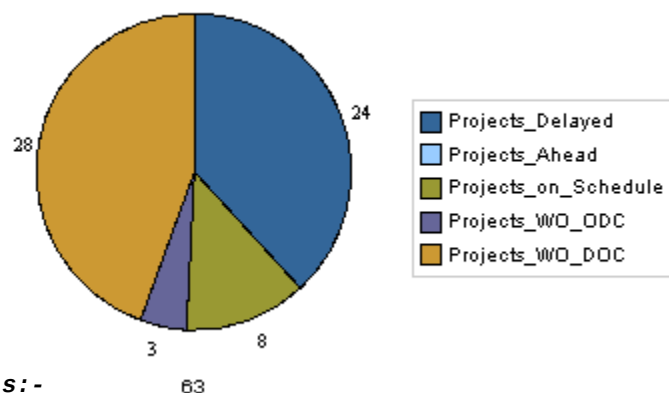


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 63 projects when sanctioned, was of the order of Rs. 186663.06 crore but this was subsequently anticipated to Rs. 193294.88 crore implying a cost overrun of 3.6%. The expenditure incurred on these projects till September, 2019 is Rs. 85310.09 crore, which is 44.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

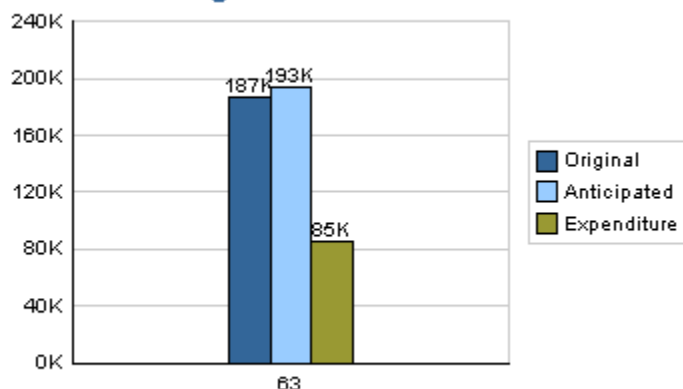

Sector wise current status of projects on the Flash Report


WATER RESOURCES

Current Status:

Number of Projects	2
Number of Projects On Schedule	1
Number of Projects Delayed	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 1 project is on schedule 1 project is delayed.

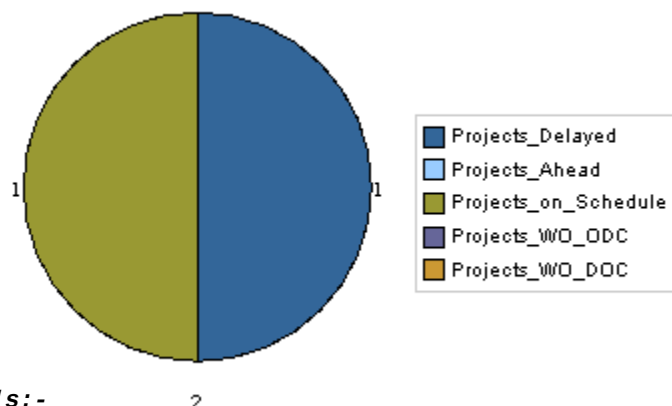

Total No Of Project's:-

2

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 10384.61 crore but this was subsequently anticipated to Rs. 55782.44 crore implying a cost overrun of 437.2%. The expenditure incurred on these projects till September, 2019 is Rs. 16450.19 crore, which is 29.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

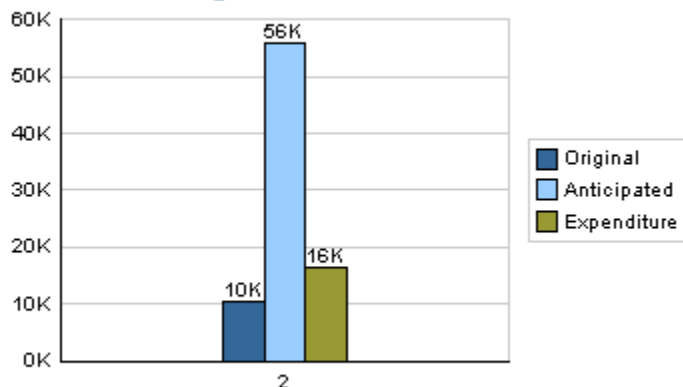


TABLE-30

Detail of ongoing Projects Costing Rs.150 Crore and above.									
						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT ,	10/2009	11,459.00 16,580.00	16,580.00	14,137.00	12/2015 -	06/2020	54(O) -	53/70
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN ,	10/2009	12,320.00 17,079.00	17,079.00	11,387.00	12/2016 -	12/2020	48(O) -	40/68
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI 500 MWE) - [020100044]BHAVNI,TAMIL NADU ,	09/2003	3,492.00 -	6,840.00	5,821.38	09/2010 -	10/2021	133(O) -	83/87
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL,TAMIL NADU , Central Sector Projects	03/2013	39,849.00 -	39,849.00	15,706.00	11/2020 -	11/2023	36(O) -	23/76
	Total		67,120.00 -	80,348.00	47,051.38				199/301
	<u>CIVIL AVIATION</u>								
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT PORTBLAIR - [N04000073]AAI,A & N ISLANDS ,	10/2013	314.61 -	441.33	85.79	09/2018 -	06/2020	21(O) -	0/0
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]AAI,ASSAM ,	12/2016	859.86 -	860.00	232.44	03/2021 -	03/2021	0(O) -	0/0
7	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES PHASE I AND II - [N04000082]AAI,BIHAR ,	05/2018	539.20 -	539.20	25.64	10/2022 -	10/2022	0(O) -	0/0
8	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA BCAS AAIB AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076]AAI,DELHI ,	11/2016	233.38 -	233.38	84.73	04/2020 -	12/2020	8(O) -	0/0
9	CONSTRUCTION OF TERMINAL BUILDING & ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]AAI,JAMMU AND KASHMIR ,	07/2018	323.19 -	323.19	10.14	09/2021 -	09/2021	0(O) -	0/0
10	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING RECONSTRUCTION OF OLD TERMINAL BUILDING MODIFICAT - [N04000079]AAI,MAHARASHTRA ,	03/2017	358.89 -	358.89	29.73	04/2021 -	04/2021	0(O) -	0/0
11	MODERNIZATION OF CHENNAI AIRPORT PHASE II CHENNAI - [N04000074]AAI,TAMIL NADU ,	06/2018	2,467.00 -	2,467.00	213.17	02/2022 -	08/2022	6(O) -	0/0
12	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]AAI,TAMIL NADU ,	08/2018	951.28 -	951.28	71.55	10/2021 -	10/2021	0(O) -	0/0
13	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI,TRIPURA ,	09/2015	338.93 -	339.00	213.50	06/2019 -	12/2019	6(O) -	0/0
14	CCS INTERNATIONAL AIRPORT LUCKNOW - [N04000077]AAI,UTTAR PRADESH ,	06/2018	1,383.00 -	1,383.00	210.62	09/2021 -	09/2021	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
15	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT DEHRADUN - [N04000085]AAI,UTTARAKHAND ,	07/2018	353.27 -	353.27	114.29	09/2020 -	09/2020	0(O) -	0/0
16	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA - [N04000080]AAI, WEST BENGAL ,	01/2016	219.91 -	219.91	61.61	03/2020 -	12/2020	9(O) -	0/0
17	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT KOLKATA - [N04000081]AAI, WEST BENGAL ,	01/2019	264.99 -	264.99	.42	11/2021 -	11/2021	0(O) -	0/0
	Total		8,607.51 -	8,734.44	1,353.63				0/0
	<u>COAL</u>								
18	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL, CHHATISGARH ,	06/2010	11,816.40 -	11,816.40	2,882.36	03/2023 -	03/2023	0(O) -	14/19
19	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL, CHHATISGARH ,	08/2013	7,612.33 -	7,612.33	2,057.57	03/2023 -	03/2023	0(O) -	7/21
20	PELMA OCP(15.00MTY) - [N06000045]SECL, CHHATISGARH ,	11/2014	1,624.59 -	1,624.59	6.42	03/2023 -	03/2023	0(O) -	1/12
21	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL, CHHATISGARH ,	09/2008	152.43 -	459.49	193.40	03/2015 -	03/2020	60(O) -	6/10
22	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH ,	07/2008	178.44 -	178.44	2.88	03/2014 -	03/2020	72(O) -	2/8
23	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH ,	12/2009	321.50 -	321.50	192.55	03/2014 -	03/2021	84(O) -	0/5
24	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL, CHHATISGARH ,	04/2012	258.56 -	258.56	180.07	03/2016 -	03/2020	48(O) -	4/7
25	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL, CHHATISGARH ,	12/2013	610.63 -	610.63	102.91	03/2022 -	03/2022	0(O) -	2/10
26	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL, CHHATISGARH ,	05/2014	164.49 -	164.49	82.91	03/2020 -	03/2020	0(O) -	5/9
27	AMERA OC RCE - [N06000123]SECL, CHHATISGARH ,	02/2015	335.97 -	335.97	51.25	03/2018 -	03/2020	24(O) -	1/7
28	AMGAON OPENCAS PROJECT RCE - [N06000135]SECL, CHHATISGARH ,	07/2015	316.10 -	316.10	73.31	03/2020 -	03/2020	0(O) -	1/6
29	DURGAPUR OPENCAS PROJECT - [N06000136]SECL, CHHATISGARH ,	02/2015	916.24 -	916.24	4.02	03/2023 -	03/2023	0(O) -	1/11
30	MADANNAGAR OPENCAS PROJECT - [N06000140]SECL, CHHATISGARH ,	10/2015	1,875.32 -	1,875.32	.00	03/2024 -	03/2024	0(O) -	1/5
31	VIJAY WEST OPENCAS PROJECT - [N06000158]SECL, CHHATISGARH ,	05/2017	976.95 -	976.95	75.96	03/2026 -	03/2026	0(O) -	0/1
32	MAHAMAYA OPENCAS PROJECT - [N06000164]SECL, CHHATISGARH ,	05/2018	410.26 -	410.26	9.53	03/2026 -	03/2026	0(O) -	0/1
33	JHIRIA WEST OPENCAS PROJECT - [N06000166]SECL, CHHATISGARH ,	11/2018	389.97 -	389.97	.00	03/2026 -	03/2026	0(O) -	1/1
34	MAGADH OC 20 MTY (CCL) - [N06000015]JCL, JHARKHAND ,	08/2008	706.40 -	706.40	354.93	07/2012 -	03/2022	116(O) -	6/6
35	CHURI BENTI UG (0.81 MTY) - [N06000083]JCL, JHARKHAND ,	08/2007	163.51 -	163.51	106.41	03/2011 -	03/2021	120(O) -	4/6
36	TAPIN OCP (2.5 MTY) - [N06000086]JCL, JHARKHAND ,	08/2008	264.68 -	264.68	181.17	03/2012 -	03/2021	108(O) -	5/6

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
37	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND ,	12/2009	510.85 -	510.85	362.49	03/2016 -	03/2021	60(O) -	5/6
38	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND ,	06/2009	162.46 -	162.46	90.78	03/2014 -	03/2021	84(O) -	6/6
39	MURAI DIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND ,	02/2011	339.88 -	339.88	12.08	04/2014 -	-	-	4/7
40	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND ,	08/2011	1,230.27 -	1,230.27	394.32	04/2015 -	-	-	2/6
41	AMRAPALI OC(12MTY) - [N06000103]CCL,JHARKHAND ,	02/2012	858.11 -	858.11	194.12	03/2020 -	03/2020	0(O) -	6/7
42	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND ,	02/2014	555.52 -	555.52	5.24	03/2021 -	03/2021	0(O) -	0/2
43	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND ,	08/2011	988.35 -	988.35	45.26	04/2017 -	-	-	1/3
44	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND ,	08/2010	289.45 -	289.45	257.56	05/2014 -	03/2020	70(O) -	0/8
45	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND ,	10/2012	269.82 -	269.82	180.83	04/2014 -	11/2019	67(O) -	0/10
46	HURA - C OC (3 MTY) - [N06000143]ECL,JHARKHAND ,	10/2015	359.69 -	359.69	83.23	03/2022 -	03/2022	0(O) -	3/22
47	CHITRA EAST (RCE) OCP - [N06000169]ECL,JHARKHAND ,	08/2018	513.98 -	513.98	90.23	03/2024 -	03/2024	0(O) -	0/16
48	NORTH URIMARI EXPANSION OCP - [N06000182]CCL,JHARKHAND ,	03/2019	1,553.06 -	1,553.06	163.23	03/2023 -	03/2023	0(O) -	0/1
49	BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH ,	08/2015	1,186.64 -	203.82	121.39	03/2023 -	03/2021	-24(O) -	3/10
50	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH ,	02/2015	481.60 -	481.60	.00	03/2023 -	03/2023	0(O) -	2/9
51	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH ,	12/2014	357.80 -	357.80	104.06	03/2021 -	03/2021	0(O) -	3/10
52	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH ,	12/2014	371.04 -	371.04	52.43	03/2021 -	03/2021	0(O) -	3/8
53	BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH ,	07/2015	231.92 -	231.92	.00	03/2022 -	03/2022	0(O) -	1/8
54	MALACHUA OPENCASST PROJECT - [N06000139]SECL,MADHYA PRADESH ,	10/2015	488.33 -	488.33	27.10	03/2023 -	03/2023	0(O) -	0/4
55	AMADAND OPENCASST EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH ,	03/2016	869.44 -	869.44	116.48	03/2021 -	03/2021	0(O) -	2/5
56	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL,MADHYA PRADESH ,	07/2016	409.87 -	409.87	20.30	03/2022 -	03/2022	0(O) -	0/0
57	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL,MADHYA PRADESH , Central Sector Projects	05/2017	1,783.09 -	1,783.09	267.80	03/2021 -	03/2021	0(O) -	1/9
58	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]NCL,MADHYA PRADESH ,	11/2017	1,255.17 -	1,255.17	95.24	03/2022 -	03/2022	0(O) -	1/9
59	SEMARIA OPENCASST PROJECT - [N06000176]NCL,MADHYA PRADESH ,	05/2019	396.58 -	396.58	.00	03/2026 -	03/2026	0(O) -	1/5
60	VISHNUPURI UG TO OC MINE - [N06000178]WCL,MADHYA PRADESH ,	07/2018	195.57 -	195.57	2.94	03/2025 -	03/2025	0(O) -	0/7
61	GANDHIGRAM UG MINE - [N06000183]WCL,MADHYA PRADESH ,	08/2019	414.16 -	414.16	.00	03/2026 -	03/2026	0(O) -	0/7

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
62	BLOCK-B EXPANSION OPENCAST PROJECT - [N06000184]NCL,MADHYA PRADESH ,	07/2019	998.71	998.71	.00	03/2023	03/2023	0(O)	0/7
63	PENGANGA OCP(REVISED) - [N06000066]WCL,MAHARASHTRA ,	09/2014	441.82	441.82	213.24	03/2020	03/2020	0(O)	8/11
64	DINESH OCP - [N06000118]WCL,MAHARASHTRA ,	11/2014	611.16	611.16	413.13	03/2020	03/2020	0(O)	3/8
65	BHANEGAON OC - [N06000121]WCL,MAHARASHTRA ,	02/2015	187.94	409.68	128.90	03/2023	03/2023	0(O)	7/11
66	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA ,	05/2015	295.56	295.56	123.60	03/2019	-	-	10/13
67	SINGHORI OC MINE - [N06000130]WCL,MAHARASHTRA ,	06/2015	205.49	205.49	121.74	03/2020	03/2020	0(O)	6/10
68	AMALGAMATED PAUNI-II III OC MINE - [N06000131]WCL,MAHARASHTRA ,	06/2015	483.69	483.69	210.32	03/2021	03/2021	0(O)	3/6
69	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]WCL,MAHARASHTRA ,	08/2015	727.28	727.28	268.58	03/2025	03/2025	0(O)	6/13
70	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA ,	08/2015	288.90	333.43	21.02	03/2023	03/2024	12(O)	3/10
71	KAMPTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA ,	11/2015	277.65	313.34	116.34	03/2021	03/2024	36(O)	3/6
72	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]WCL,MAHARASHTRA ,	11/2015	498.42	498.42	182.76	03/2020	03/2020	0(O)	2/6
73	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL,MAHARASHTRA ,	02/2016	198.68	198.68	184.77	03/2019	-	-	3/9
74	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA ,	02/2016	304.52	304.52	153.29	03/2019	-	-	3/8
75	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL,MAHARASHTRA ,	03/2017	362.73	362.73	319.93	03/2020	03/2020	0(O)	0/0
76	SAONER I UG TO OC PHASE I - [N06000177]WCL,MAHARASHTRA ,	11/2016	162.10	162.10	50.56	03/2022	03/2022	0(O)	0/6
77	UKNI DEEP OC - [N06000179]WCL,MAHARASHTRA ,	11/2018	318.14	318.14	146.45	03/2021	03/2021	0(O)	0/4
78	BELLORA-NAIGAON DEEP OC - [N06000180]WCL,MAHARASHTRA ,	11/2018	252.71	252.71	44.94	03/2021	03/2021	0(O)	0/3
79	GAURI DEEP OC - [N06000181]WCL,MAHARASHTRA ,	10/2016	164.96	164.96	93.37	03/2019	-	-	1/3
80	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]WCL,MULTI STATE ,	08/2016	319.76	319.76	235.33	03/2022	03/2022	0(O)	0/3
81	DHANKASA UG (1.00 MTY) - [N06000155]WCL,MULTI STATE ,	09/2016	458.07	458.07	20.86	03/2022	03/2022	0(O)	1/12
82	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL,MULTI STATE ,	02/2017	328.00	328.00	160.15	03/2021	03/2021	0(O)	2/6
83	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA ,	01/2005	302.96	302.96	302.96	03/2010	03/2020	120(O)	10/10
84	BHUBANESWARI OCP MCL (20.0 MTY) - [N06000034]MCL,ODISHA ,	12/2007	490.10	490.10	501.82	03/2017	03/2020	36(O)	11/12
85	KANIHA OCP MCL (10.0 MTY) - [N06000035]MCL,ODISHA ,	12/2007	457.77	457.77	539.59	03/2013	03/2022	108(O)	8/9
86	BALRAM OCP EXTENSION MCL 8.00 MTY - [N06000044]MCL,ODISHA ,	12/2007	172.08	172.08	347.15	03/2010	03/2022	144(O)	3/4

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
87	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA ,	08/2008	207.28 -	207.28	228.90	03/2012 -	03/2021	108(O) -	5/7
88	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA ,	11/2008	479.53 -	479.53	390.94	03/2013 -	03/2021	96(O) -	6/9
89	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA ,	05/2014	479.15 -	479.15	200.65	03/2019 -	03/2022	36(O) -	2/9
90	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA ,	05/2014	3,756.36 -	3,756.36	1,549.76	03/2026 -	03/2026	0(O) -	7/15
91	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA ,	05/2014	337.66 -	337.66	183.98	03/2019 -	03/2020	12(O) -	5/6
92	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA ,	06/2014	289.03 -	289.03	75.85	03/2018 -	03/2020	24(O) -	4/6
93	GARJANBAHAL OCP - [N06000117]MCL,ODISHA ,	11/2014	1,375.38 -	1,375.38	440.13	03/2021 -	03/2021	0(O) -	6/9
94	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]MCL,ODISHA ,	05/2018	2,434.75 -	2,434.75	83.20	03/2027 -	03/2027	0(O) -	2/12
95	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]MCL,ODISHA ,	11/2018	2,838.87 -	2,838.87	1,113.66	03/2029 -	03/2029	0(O) -	0/9
96	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN , Central Sector Projects	03/2015	522.45 -	522.45	9.88	09/2019 -	-	-	0/0
97	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN , Central Sector Projects	03/2015	513.63 -	513.63	175.30	12/2019 -	-	-	0/0
98	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU ,	06/2011	5,907.11 - 7,080.41	7,080.41	6,730.63	12/2015 -	12/2019	48(O) -	31/35
99	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU ,	04/2013	1,458.17 -	709.06	454.23	06/2015 -	-	-	5/7
100	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA ,	10/2006	249.03 -	448.86	286.19	03/2012 -	03/2024	144(O) -	35/42
101	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA ,	12/2008	453.63 -	453.63	121.91	12/2012 -	-	-	11/44
102	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA ,	12/2009	418.97 -	489.62	343.10	03/2012 -	03/2023	132(O) -	0/2
103	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA ,	03/2010	209.78 -	209.78	154.58	03/2015 -	03/2020	60(O) -	30/31
104	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA ,	03/2010	181.19 -	181.19	170.60	03/2012 -	-	-	6/6
105	KISTARAM OCP - [N06000089]SCCL,TELANGANA ,	11/2010	242.29 -	164.04	119.59	03/2015 -	03/2021	72(O) -	2/5
106	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA ,	07/2011	162.76 -	349.28	8.00	03/2015 -	03/2021	72(O) -	4/29
107	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA ,	07/2011	447.06 -	473.22	18.35	03/2015 -	03/2021	72(O) -	8/13
108	RG OC -III EXTENSION (PHASE-II) PROJECT - [N06000100]SCCL,TELANGANA ,	06/2012	365.01 -	365.01	135.62	06/2015 -	03/2020	57(O) -	36/36
109	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA ,	07/2012	417.33 -	384.32	103.95	07/2016 -	03/2020	44(O) -	25/28
110	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA ,	11/2012	430.45 -	415.37	166.43	03/2016 -	03/2020	48(O) -	38/39
111	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]SCCL,TELANGANA ,	05/2015	397.09 -	442.42	92.46	03/2019 -	03/2020	12(O) -	15/18

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
112	KOYAGUDEM OPENCASE PROJECT - [N06000146]SCCL, TELANGANA , Central Sector Projects	10/2015	426.79 -	426.79	.72	03/2018 -	03/2020	24(O) -	0/9
113	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]SCCL, TELANGANA ,	12/2015	477.65 -	477.65	2.11	03/2020 -	03/2020	0(O) -	5/17
114	KAKATIYAKHANI OPENCASE III PROJECT PHASE-1 - [N06000161]SCCL, TELANGANA ,	03/2017	413.84 -	413.84	54.51	03/2019 -	03/2022	36(O) -	1/11
115	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL, TELANGANA ,	11/2016	272.73 -	272.73	162.62	- 04/2017	03/2020	- 0	0/6
116	RAMPURAM SHAFT BLOCK - [N06000174]SCCL, TELANGANA ,	08/2016	431.92 -	431.92	.00	- 03/2023	-	-	0/9
117	SRAVANAPALLI OPENCASE PROJECT - [N06000175]SCCL, TELANGANA ,	02/2018	412.70 -	412.70	.11	- 03/2023	-	-	0/7
118	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC, UTTAR PRADESH ,	07/2016	17,237.00 -	17,237.80	7,532.67	11/2021 -	11/2021	0(O) -	0/0
119	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]ECL, WEST BENGAL ,	11/2015	602.86 -	602.86	315.69	03/2022 -	03/2022	0(O) -	9/13
120	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL, WEST BENGAL ,	08/2012	1,055.05 -	1,055.05	510.31	03/2018 -	10/2020	31(O) -	11/16
121	RANIGANJ MASTER PLAN - [N06000163]ECL, WEST BENGAL ,	08/2009	2,661.73 -	5,186.24	330.94	08/2019 -	-	-	0/19
122	SIDULI MINE (OC AND UG) - [N06000165]ECL, WEST BENGAL ,	05/2018	535.18 -	535.18	.00	03/2026 -	03/2026	0(O) -	0/22
123	NAKRAKONDA KUMARDI B OCP - [N06000170]ECL, WEST BENGAL ,	08/2018	502.68 -	502.68	.00	03/2029 -	03/2029	0(O) -	0/22
124	TILABONI UG MINE - [N06000172]ECL, WEST BENGAL ,	02/2019	916.62 -	916.62	.00	03/2027 -	03/2027	0(O) -	0/27
	Total		1,04,997.33 -	1,07,975.18	36,413.13				507/1121
	<u>FERTILISERS</u>								
125	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]NFL, HARYANA ,	01/2018	215.92 -	215.92	117.03	11/2019 -	11/2019	0(O) -	0/2
126	NEW SEWAGE TREATMENT PLANT PACKAGE RCF TROMBAY - [N08000009]RCF, MAHARASHTRA ,	10/2014	197.79 -	209.44	174.52	11/2016 -	09/2019	34(O) -	3/13
127	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]RCF, MAHARASHTRA ,	04/2018	426.72 -	426.72	197.47	04/2020 -	04/2020	0(O) -	1/14
128	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]NFL, PUNJAB ,	01/2018	218.83 -	218.83	119.23	11/2019 -	11/2019	0(O) -	0/2
129	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]NFL, PUNJAB ,	01/2018	239.81 -	239.81	134.46	11/2019 -	11/2019	0(O) -	0/2
	Total		1,299.07 -	1,310.72	742.71				4/33
	<u>INFORMATION AND BROADCASTING</u>								

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
130	FILM AND TELEVISION INSTITUTE ARUNACHAL PRADESH - [N09000002]CPWD,ANDHRA PRADESH ,	11/2016	204.32 -	204.32	.00	02/2019 -	11/2019	9(O) -	0/0
131	NATIONAL FILM HERITAGE MISSION - [N09000001]NFAI,MAHARASHTRA ,	11/2014	597.41 -	597.41	29.80	- -	-	-	0/0
132	NATIONAL CENTRE OF EXCELLENCE FOR ANIMATION VISUAL EFFECTS GAMING AND COMICS - [N09000003]NBCC,MAHARASHTRA ,	12/2016	167.70 -	167.70	.00	03/2020 -	03/2020	0(O) -	0/0
	Total		969.43 -	969.43	29.80				0/0
	<u>MINES</u>								
133	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]NALCO,ODISHA ,	12/2014	5,540.00 5,540.00	5,540.00	107.45	04/2021 04/2021	04/2021	0(O) 0	3/3
134	UTKAL D AND E COAL BLOCK - [N10000011]NALCO,ODISHA ,	05/2016	534.00 -	534.00	319.23	01/2020 -	01/2020	0(O) -	1/2
135	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]NALCO,ODISHA , Central Sector Projects	12/2015	355.00 -	355.00	31.92	11/2020 -	11/2020	0(O) -	2/2
136	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]NALCO,ODISHA , Central Sector Projects	11/2017	483.00 483.00	483.00	.30	04/2021 04/2021	04/2021	0(O) 0	1/1
137	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]NALCO,TAMIL NADU ,	09/2017	166.62 -	166.62	134.98	06/2019 -	-	-	1/1
	Total		7,078.62 -	7,078.62	593.88				8/9
	<u>STEEL</u>								
138	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH ,	12/2011	2,858.00 -	2,500.00	1,400.76	12/2017 10/2019	10/2019	22(O) 0	5/6
139	CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH ,	08/2015	320.66 -	320.66	220.91	08/2018 10/2019	10/2019	14(O) 0	3/4
140	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH ,	01/2010	15,525.00 -	23,140.00	16,064.29	05/2015 07/2020	07/2020	62(O) 0	65/86
141	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND ,	03/2015	1,034.01 -	1,034.01	436.08	10/2017 06/2020	06/2020	32(O) 0	0/2
142	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND ,	05/2015	1,154.18 -	1,154.18	963.95	12/2017 11/2019	11/2019	23(O) 0	1/2
143	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND ,	11/2016	262.87 -	262.87	104.85	06/2019 06/2020	06/2020	12(O) 0	0/1
144	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA ,	04/2015	3,127.30 -	3,127.30	3,031.06	04/2018 11/2019	11/2019	19(O) 0	3/3
145	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH ,	04/2014	1,682.85 -	1,682.85	1,227.53	09/2018 10/2019	10/2019	13(O) 1	4/5
146	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E - [N12000121]SAIL,WEST BENGAL ,	12/2018	263.36 -	263.36	11.32	09/2020 -	09/2020	0(O) -	0/4

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	Total		26,228.23	33,485.23	23,460.75				81/113
	<u>PETROLEUM</u>								
147	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH ,	07/2016	20,928.00	20,928.00	6,455.02	07/2020	07/2020	0(O)	84/111
148	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH ,	03/2016	34,012.00	34,012.00	3,411.92	06/2020	08/2021	14(O)	15/20
149	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL,ANDHRA PRADESH ,	01/2015	342.00	342.00	.00	03/2021	03/2021	0(O)	0/0
150	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL,ANDHRA PRADESH ,	07/2014	247.00	247.00	.00	03/2021	03/2021	0(O)	0/0
151	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003 NAGAYALANKA-KG - [N16000280]ONGC,ANDHRA PRADESH ,	04/2017	420.76	407.45	239.45	09/2018	09/2019	12(O)	4/5
152	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL AP - [N16000302]IOCL,ANDHRA PRADESH ,	08/2017	384.58	384.58	85.86	04/2021	04/2020	-12(O)	0/0
153	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH ,	08/2018	466.00	466.00	84.34	04/2021	07/2021	3(O)	0/0
154	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH ,	04/2018	355.00	355.00	14.07	04/2022	02/2023	10(O)	0/0
155	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]IOCL,ANDHRA PRADESH ,	10/2018	316.20	316.20	14.78	10/2021	10/2021	0(O)	0/0
156	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364]BPCL,ANDHRA PRADESH ,	07/2017	580.20	580.20	38.21	02/2021	02/2021	0(O)	0/16
157	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM ,	03/2009	2,465.15	2,378.86	2,147.00	03/2013	12/2019	81(O)	6/15
158	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM ,	06/2010	202.94	345.92	146.58	01/2014	11/2019	70(O)	6/7
159	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) CACHAR ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM ,	06/2016	423.00	423.00	263.70	08/2019	09/2019	1(O)	5/13
160	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]IOCL,ASSAM ,	02/2016	2,582.00	2,582.00	1,557.14	11/2019	11/2019	0(O)	13/17
161	PIPELINE NETWORK PROJECT GELEKI ASSAM - [N16000278]ONGC,ASSAM ,	07/2016	249.85	265.49	157.81	05/2020	05/2020	0(O)	4/5
162	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM ,	07/2011	350.00	350.00	2.06	01/2019	09/2019	8(O)	0/0
163	BS-VI PROJECT AT BONGAIGAON REFINERY - [N16000320]IOCL,ASSAM ,	05/2018	1,222.00	1,222.00	563.53	09/2019	02/2020	5(O)	6/7
164	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM ,	01/2018	543.91	682.90	8.97	02/2020	06/2020	4(O)	1/14
165	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]IOCL,ASSAM ,	08/2018	557.00	557.00	217.83	02/2020	02/2020	0(O)	2/5

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
166	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS MADHUBAN - [N16000356]OIL, ASSAM ,	06/2016	224.75 -	224.75	4.37	08/2020 -	08/2020	0(O) -	0/0
167	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL, ASSAM ,	09/2012	871.35 -	1,200.00	565.63	03/2015 -	-	-	0/5
168	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]IOCL, BIHAR ,	07/2015	822.66 -	822.66	822.02	11/2018 -	08/2019	-	8/8
169	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]IOCL, BIHAR ,	05/2016	664.00 -	664.00	601.75	12/2020 -	02/2020	-10(O) -	4/5
170	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]IOCL, BIHAR ,	09/2015	324.00 -	324.00	154.50	06/2020 -	03/2020	-3(O) -	3/4
171	LPG BP PROJECT MOTIHARI - [N16000317]IOCL, BIHAR ,	05/2018	206.50 -	206.50	13.88	03/2021 -	03/2021	0(O) -	11/26
172	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]IOCL, BIHAR ,	12/2017	199.36 -	199.36	9.39	10/2020 -	10/2020	0(O) -	2/2
173	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]GAIL, BIHAR ,	10/2017	359.25 -	359.25	68.16	10/2022 -	10/2022	0(O) -	0/0
174	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]IOCL, BIHAR ,	07/2018	189.00 -	189.00	9.15	01/2021 -	01/2021	0(O) -	2/8
175	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI BIHAR - [N16000344]IOCL, BIHAR ,	04/2018	522.00 -	522.00	142.71	03/2021 -	03/2021	0(O) -	0/0
176	FUEL QUALITY UPGRADATION (NSU NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY - [N16000348]IOCL, BIHAR ,	06/2017	951.64 -	951.64	399.12	10/2019 -	10/2019	0(O) -	9/11
177	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH - [N16000311]HPCL, CHHATTISGARH ,	12/2016	300.00 -	300.00	1.09	04/2021 -	-	-	0/0
178	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC, D & N HAVELI ,	08/2014	6,086.08 5,842.31	5,842.31	4,784.88	05/2019 10/2019	10/2019	5(O) 0	13/14
179	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL, GUJARAT ,	04/2016	327.78 -	200.00	146.50	04/2018 -	10/2019	18(O) -	18/20
180	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]ONGC, GUJARAT ,	02/2017	1,162.56 -	1,162.56	392.39	03/2026 -	03/2026	0(O) -	7/10
181	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]IOCL, GUJARAT , Central Sector Projects	09/2016	208.35 -	208.35	123.99	07/2020 -	07/2020	0(O) -	10/10
182	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309]IOCL, GUJARAT ,	08/2017	1,342.00 -	1,342.00	6.30	08/2020 -	08/2020	0(O) -	1/1
183	BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]IOCL, GUJARAT ,	03/2018	3,380.00 -	3,380.00	2,102.63	09/2019 -	03/2020	6(O) -	7/9
184	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL, GUJARAT ,	10/2017	906.00 -	906.00	93.08	02/2020 -	10/2020	8(O) -	4/8
185	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA GUJARAT - [N16000336]IOCL, GUJARAT ,	03/2018	588.20 -	588.20	.94	-	08/2022	-	8/17

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
186	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]GAIL,GUJARAT ,	09/2018	225.54 -	225.54	1.41	02/2021 -	02/2021	0(O) -	2/8
187	GAS COMPRESSOR PROJECT AT ANKLESHWAR ASSET (GCP-ANK) - [N16000371]ONGC,GUJARAT ,	10/2018	156.67 -	156.67	.00	03/2021 -	03/2021	0(O) -	0/6
188	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]HPCL,HARYANA ,	11/2017	255.00 -	255.00	75.50	11/2020 -	11/2020	0(O) -	19/46
189	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]IOCL,HARYANA ,	04/2018	206.63 -	206.63	13.75	02/2020 -	02/2020	0(O) -	4/6
190	BS-VI PROJECT AT PANIPAT REFINERY - [N16000325]IOCL,HARYANA ,	12/2017	3,529.00 -	3,529.00	1,720.28	07/2019 -	12/2019	5(O) -	9/9
191	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]IOCL,HARYANA ,	08/2018	1,636.00 -	1,636.00	148.87	08/2020 -	08/2020	0(O) -	4/6
192	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]IOCL,HARYANA ,	01/2019	909.00 -	909.00	16.17	01/2021 -	01/2021	0(O) -	0/0
193	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]IOCL,HARYANA ,	10/2018	598.00 -	598.00	15.22	02/2020 -	02/2020	0(O) -	3/4
194	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]GAIL,HARYANA ,	08/2018	286.42 -	286.42	1.93	08/2020 09/2020	09/2020	1(O) 0	6/16
195	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV PANIPAT - [N16000363]IOCL,HARYANA ,	12/2018	278.60 -	278.60	.00	06/2021 -	06/2021	0(O) -	0/3
196	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]IOCL,HIMACHAL PRADESH ,	02/2016	151.00 -	151.00	147.35	09/2019 -	-	-	4/4
197	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]ONGC,JHARKHAND ,	12/2015	823.27 910.23	910.23	356.00	03/2023 03/2022	03/2022	-12(O) 0	6/10
198	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]HPCL,JHARKHAND ,	06/2017	161.50 -	161.50	17.78	06/2020 -	09/2021	15(O) -	0/0
199	CITY GAS DISTRIBUTION (CGD) NETWORK RANCHI - [N16000329]GAIL,JHARKHAND ,	10/2017	226.45 -	226.45	50.15	10/2022 -	10/2022	0(O) -	11/17
200	CITY GAS DISTRIBUTION (CGD) NETWORK JAMSHEDPUR - [N16000330]GAIL,JHARKHAND ,	10/2017	221.45 -	221.45	46.15	10/2022 -	10/2022	0(O) -	0/0
201	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]BPCL,JHARKHAND ,	11/2018	248.55 -	248.55	22.86	06/2022 -	06/2022	0(O) -	0/0
202	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPR,KARNATAKA ,	01/2006	993.00 -	1,693.00	1,549.85	01/2012 -	-	-	0/0
203	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA , Central Sector Projects	02/2015	749.00 -	842.00	606.89	02/2020 -	02/2020	0(O) -	0/0
204	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]MANGALORE REFIN,KARNATAKA ,	05/2015	224.00 207.00	185.00	164.61	04/2019 -	-	-	8/8
205	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]MANGALORE REFIN,KARNATAKA ,	10/2015	135.00 170.70	170.70	156.65	03/2019 10/2019	10/2019	7(O) 0	11/11
206	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA ,	09/2016	1,810.00 1,810.00	1,810.00	823.40	12/2019 07/2020	07/2020	7(O) 0	8/9

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
207	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA , Central Sector Projects	11/2017	581.00 -	621.00	84.47	03/2020 -	09/2020	6(O) -	2/3
208	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]BPCL,KARNATAKA ,	10/2018	206.26 -	206.26	.98	03/2021 -	03/2021	0(O) -	0/0
209	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367]HPCL,KARNATAKA ,	06/2019	2,166.38 -	2,166.38	9.80	06/2022 -	06/2022	0(O) -	0/18
210	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369]HPCL,KARNATAKA ,	12/2018	854.00 -	854.00	38.34	12/2022 -	12/2022	0(O) -	0/0
211	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA ,	10/2015	607.06 -	714.25	355.48	10/2017 -	-	-	39/52
212	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA ,	11/2014	4,588.29 5,245.96	5,245.96	3,711.38	08/2018 11/2019	11/2019	15(O) 0	0/20
213	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA ,	02/2016	3,313.00 3,288.96	3,288.96	1,151.10	02/2020 10/2020	10/2020	8(O) 0	0/20
214	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA ,	12/2015	1,112.00 1,507.24	1,507.24	525.00	06/2019 02/2022	02/2022	32(O) 0	0/0
215	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]BPCL,KERALA ,	09/2018	11,130.00 -	11,130.00	18.14	03/2023 -	03/2023	0(O) -	0/0
216	PROVISION OF 2ND SPUR FOR TWL GANTRY TWD FACILITY FOR MS AND HSD ADDITIONAL TANKS FOR MS HSD AND - [N16000304]IOCL,MADHYA PRADESH ,	08/2017	236.00 -	236.00	24.15	06/2020 -	08/2020	2(O) -	0/0
217	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA ,	03/2011	861.79 -	1,683.06	1,322.31	05/2013 12/2019	12/2019	79(O) 0	4/8
218	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA ,	12/2011	2,059.63 2,665.65	2,665.65	1,908.01	03/2015 12/2019	12/2019	57(O) 0	15/18
219	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA ,	11/2014	6,068.80 -	5,296.93	4,758.62	04/2019 12/2019	12/2019	8(O) 0	8/9
220	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA ,	08/2015	2,818.88 -	2,818.88	2,230.96	03/2019 05/2020	05/2020	14(O) 0	4/5
221	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA BASSEIN AND PANNA - [N16000212]ONGC,MAHARASHTRA , Central Sector Projects	01/2015	4,619.94 -	4,619.94	4,360.59	12/2017 03/2020	03/2020	27(O) 0	4/5
222	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA , Central Sector Projects	12/2015	3,190.69 -	3,247.19	2,225.67	04/2018 05/2020	05/2020	25(O) 0	13/15
223	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL,MAHARASHTRA ,	05/2016	1,945.00 -	1,945.00	960.09	08/2021 -	08/2021	0(O) -	4/5
224	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]BPCL,MAHARASHTRA ,	02/2016	554.00 -	554.00	363.86	02/2020 -	10/2019	-4(O) -	0/10
225	MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL,MAHARASHTRA ,	04/2013	449.58 -	449.58	155.32	12/2019 -	12/2019	0(O) -	0/17

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
226	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA ,	05/2016	212.00 -	212.00	38.55	01/2021 -	04/2021	3(O) -	0/0
227	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA ,	05/2016	348.00 -	348.00	30.75	01/2021 -	10/2021	9(O) -	0/0
228	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL,MAHARASHTRA ,	05/2016	261.00 -	261.00	41.42	01/2021 -	01/2021	0(O) -	0/0
229	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL,MAHARASHTRA ,	09/2015	4,199.00 5,060.00	5,060.00	2,754.00	03/2020 -	03/2020	0(O) -	107/135
230	DEVELOPMENT OF B-147 FIELD - [N16000292]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	546.15 565.15	565.15	442.18	11/2019 03/2020	03/2020	4(O) 0	4/5
231	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	511.30 -	511.30	476.47	11/2019 -	11/2019	0(O) -	4/5
232	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	968.61 -	1,033.95	930.62	11/2019 -	11/2019	0(O) -	4/5
233	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]ONGC,MAHARASHTRA ,	02/2017	4,006.83 -	4,475.92	2,796.50	05/2021 12/2021	12/2021	7(O) 0	11/15
234	PUNE POL STORAGE DEPOT - [N16000313]BPCL,MAHARASHTRA ,	08/2016	282.64 -	282.64	127.11	08/2020 -	08/2020	0(O) -	0/15
235	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD) MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA ,	06/2017	249.26 -	249.26	60.45	06/2020 -	09/2021	15(O) -	0/0
236	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) - [N16000335]ONGC,MAHARASHTRA ,	04/2018	766.37 -	766.37	449.88	12/2019 -	12/2019	0(O) -	4/5
237	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3 D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]ONGC,MAHARASHTRA ,	02/2019	2,292.46 -	2,292.46	300.13	05/2021 -	05/2021	0(O) -	4/6
238	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]ONGC,MAHARASHTRA ,	04/2019	3,228.80 -	3,228.80	458.52	03/2022 -	03/2022	0(O) -	4/6
239	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]ONGC,MAHARASHTRA ,	02/2019	3,660.71 3,740.05	3,740.05	126.66	04/2021 -	05/2021	1(O) -	4/6
240	HEERA REDEVELOPMENT - PHASE III - [N16000360]ONGC,MAHARASHTRA ,	05/2019	2,494.68 -	2,494.68	.00	12/2021 -	03/2022	3(O) -	4/6
241	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]ONGC,MAHARASHTRA ,	05/2019	763.92 -	763.92	.00	12/2020 -	12/2020	0(O) -	4/5
242	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE ,	07/2011	352.56 -	438.84	230.43	03/2017 -	12/2019	33(O) -	2/15
243	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE ,	01/2015	1,823.00 3,027.90	3,027.90	861.98	12/2020 -	12/2020	0(O) -	4/5
244	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE ,	01/2015	2,321.00 3,338.00	3,338.00	1,820.56	12/2020 -	08/2020	-4(O) -	4/5

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
245	JAIPUR-PANIPAT NAPTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE ,	02/2015	890.00 -	887.00	603.29	10/2019 -	10/2019	0(O) -	5/6
246	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE ,	01/2015	690.00 -	690.00	299.12	07/2018 -	10/2020	27(O) -	24/36
247	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]HPCL,MULTI STATE ,	09/2016	1,879.00 -	1,879.00	1,476.87	06/2020 -	06/2020	0(O) -	18/24
248	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE ,	05/2016	406.00 -	406.00	88.85	10/2020 -	10/2020	0(O) -	6/12
249	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE ,	09/2016	571.66 -	571.66	200.97	12/2019 -	12/2019	0(O) -	6/22
250	LAYING OF VIJAIIPUR-AURAIYA PIPELINE SECTION OF VIJAIIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE ,	07/2015	2,881.40 -	2,000.00	1,285.47	12/2020 -	12/2020	0(O) -	19/24
251	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]GAIL,MULTI STATE ,	03/2017	2,433.00 -	2,433.00	1,441.96	12/2020 -	12/2020	0(O) -	16/24
252	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]GAIL,MULTI STATE ,	03/2017	3,437.00 -	3,437.00	1,271.51	12/2020 -	12/2020	0(O) -	17/24
253	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE , Central Sector Projects	06/2009	2,915.00 2,915.00	3,049.47	2,524.91	12/2012 -	02/2022	110(O) -	19/42
254	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]HPCL,MULTI STATE ,	09/2017	2,677.00 -	2,677.00	894.02	03/2021 -	03/2021	0(O) -	10/26
255	50MW WIND ENERGY POWER PROJECT - [N16000298]OIL,MULTI STATE ,	11/2015	500.00 -	500.00	.00	06/2017 -	-	-	0/0
256	BARAUNI-GUWAHATI PIPELINE - [N16000334]GAIL,MULTI STATE ,	06/2018	3,308.00 -	3,308.00	1,250.10	12/2021 -	12/2021	0(O) -	10/20
257	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA ,	03/2014	3,150.00 -	3,150.00	2,573.02	09/2017 -	07/2019	-	6/6
258	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]GAIL,ODISHA ,	03/2017	1,933.00 -	1,933.00	1,035.77	12/2020 -	12/2020	0(O) -	18/24
259	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]IOCL,ODISHA ,	05/2016	429.00 -	429.00	311.78	01/2019 -	12/2019	11(O) -	6/6
260	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA , Central Sector Projects	12/2016	161.59 -	161.59	38.29	12/2019 -	07/2021	19(O) -	17/26
261	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL,ODISHA , Central Sector Projects	07/2017	243.53 -	243.53	52.38	07/2022 -	07/2022	0(O) -	0/0
262	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]IOCL,ODISHA ,	08/2017	315.00 -	315.00	112.13	12/2021 -	12/2020	-12(O) -	2/3
263	CITY GAS DISTRIBUTION (CGD) NETWORK CUTTACK - [N16000328]GAIL,ODISHA ,	07/2017	182.20 -	182.20	30.42	07/2022 -	07/2022	0(O) -	0/0
264	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]IOCL,ODISHA ,	04/2018	5,654.00 -	5,654.00	344.69	10/2021 -	10/2021	0(O) -	2/10
265	2G ETHANOL BIO REFINERY AT BARGARH - [N16000341]BPCL,ODISHA ,	08/2017	750.00 -	750.00	34.73	12/2020 -	12/2020	0(O) -	0/14

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
266	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]IOCL,ODISHA ,	10/2018	1,297.50 -	1,297.50	10.17	10/2021 -	10/2021	0(O) -	0/1
267	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]IOCL,ODISHA ,	11/2018	462.30 -	462.30	.00	09/2021 -	09/2021	0(O) -	0/0
268	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]IOCL,ODISHA ,	05/2019	3,361.00 -	3,361.00	325.72	08/2021 -	08/2021	0(O) -	3/11
269	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]IOCL,ODISHA ,	06/2019	371.00 -	371.00	.00	09/2022 -	09/2022	0(O) -	0/0
270	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN ,	11/2011	310.00 -	370.00	17.84	03/2013 -	-	-	0/24
271	LPG BP PROJECT JODHPUR - [N16000318]IOCL,RAJASTHAN ,	03/2018	229.80 -	229.80	69.24	-	03/2021	-	9/26
272	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU ,	05/2013	711.00 -	711.00	11.12	06/2020 -	06/2020	0(O) -	0/0
273	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU ,	03/2013	3,110.36 -	3,110.36	2,915.00	11/2015 -	-	-	52/52
274	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU ,	11/2012	678.00 -	678.00	5.57	02/2017 -	10/2021	56(O) -	0/0
275	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU ,	11/2015	650.82 -	650.82	394.21	03/2019 05/2020	05/2020	14(O) 0	4/5
276	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU ,	05/2016	4,497.00 6,025.00	6,025.00	499.65	12/2018 -	02/2021	26(O) -	4/5
277	AUGMENTATION OF CTMPL - [N16000286]IOCL,TAMIL NADU , Central Sector Projects	12/2016	228.00 -	228.00	15.40	06/2020 -	06/2020	0(O) -	4/5
278	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU ,	09/2017	1,858.00 -	1,858.00	1,026.86	12/2019 -	12/2019	0(O) -	0/0
279	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU ,	08/2017	421.00 -	421.00	137.46	08/2020 -	08/2020	0(O) -	0/0
280	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR TAMIL NADU - [N16000305]IOCL,TAMIL NADU ,	12/2017	466.43 -	466.43	30.95	10/2020 -	08/2021	10(O) -	0/0
281	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA ,	12/2018	611.00 -	611.00	1.68	04/2022 -	04/2022	0(O) -	0/0
282	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]GAIL,UTTAR PRADESH , Central Sector Projects	04/2017	287.49 -	287.49	125.82	04/2022 -	04/2022	0(O) -	35/43
283	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH ,	08/2017	318.80 -	318.80	40.06	08/2021 -	11/2021	3(O) -	0/0
284	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]IOCL,UTTAR PRADESH ,	01/2018	666.64 -	666.64	431.71	09/2019 -	01/2020	4(O) -	5/6
285	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]IOCL,UTTAR PRADESH ,	08/2017	255.40 -	255.40	1.75	08/2020 -	08/2020	0(O) -	1/1
286	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]IOCL,UTTAR PRADESH ,	03/2018	676.00 -	676.00	168.18	12/2021 -	12/2021	0(O) -	2/3

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
287	120 TMTPL LPG BOTTLING PLANT AT GORAKHPUR UP - [N16000354]IOCL,UTTAR PRADESH ,	03/2014	204.00 -	204.00	139.25	09/2019 -	09/2019	0(O) -	2/6
288	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL - [N16000365]BPCL,UTTAR PRADESH ,	12/2017	1,524.06 -	1,524.06	13.73	12/2021 -	12/2021	0(O) -	0/0
289	REDEVELOPMENT/ EXPANSION OF MEERUT DEPOT FOR ENHANCING PRODUCT HANDLING CAPACITY - [N16000366]HPCL,UTTAR PRADESH ,	08/2016	154.84 -	154.84	120.67	11/2019 -	11/2019	0(O) -	37/40
290	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND , Central Sector Projects	02/2017	160.10 -	160.10	41.22	02/2020 -	10/2020	8(O) -	18/26
291	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL,WEST BENGAL ,	03/2015	694.00 1,097.54	1,097.54	700.96	10/2018 12/2019	12/2019	14(O) 0	0/15
292	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL,WEST BENGAL ,	04/2016	1,021.00 -	1,021.00	4.45	12/2020 -	12/2020	0(O) -	0/0
293	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]GAIL,WEST BENGAL ,	03/2017	1,740.00 -	1,740.00	275.95	12/2020 -	12/2020	0(O) -	12/24
294	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL,WEST BENGAL ,	04/2017	163.02 -	163.02	50.84	04/2020 -	03/2021	11(O) -	17/26
295	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY - [N16000322]IOCL,WEST BENGAL ,	05/2018	2,934.40 -	2,934.40	1,653.76	09/2019 -	01/2020	4(O) -	10/11
296	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]IOCL,WEST BENGAL ,	03/2018	3,712.00 -	3,696.00	309.62	09/2022 -	06/2021	-15(O) -	1/1
	Total		2,45,939.08 -	2,53,886.39	93,345.17				1022/1680
	<u>POWER</u>								
297	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH ,	09/2003	6,285.33 -	19,496.34	10,989.45	09/2010 -	-	-	0/0
298	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH ,	12/2004	2,496.90 7,927.34	7,927.34	7,579.17	12/2009 10/2019	10/2019	118(O) 0	30/30
299	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR ,	02/2005	8,692.97 21,312.11	21,312.11	16,453.44	10/2011 08/2021	08/2021	118(O) 0	29/47
300	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR ,	01/2007	5,353.00 -	9,996.59	7,918.78	07/2012 -	09/2020	98(O) -	12/25
301	NPGCL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR , Joint Venture	01/2013	12,964.60 17,304.00	17,304.00	13,970.00	05/2018 12/2021	03/2021	34(O) -9	36/45
302	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]SJVN,BIHAR ,	03/2019	10,439.09 10,439.09	10,439.09	780.04	01/2024 -	01/2024	0(O) -	16/19
303	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH ,	12/2012	11,846.00 -	12,739.82	12,457.15	10/2017 03/2020	03/2020	29(O) 0	37/41
304	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH ,	09/2015	3,004.00 -	3,004.00	1,610.00	11/2019 -	11/2019	0(O) -	0/0
305	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI ,	03/2015	1,394.52 -	1,394.52	427.71	05/2017 -	12/2019	31(O) -	4/9
306	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT , Central Sector Projects	05/2017	175.64 -	175.64	100.00	09/2018 -	12/2019	15(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
307	SUPPLEMENTARY TRANS. SYSTEM FOR UMSP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT ,	12/2017	193.14 -	193.14	97.26	06/2019 -	12/2019	6(O) -	0/0
308	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH ,	09/2002	3,919.59 -	9,997.11	7,642.51	09/2009 -	12/2021	147(O) -	3/5
309	KIRU HYDRO ELECTRIC PROJECT - [N18000278]CVPPPL,JAMMU AND KASHMIR ,	03/2019	4,287.59 -	4,287.59	.00	- -	-	-	0/0
310	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND ,	02/2014	14,366.58 -	15,164.05	9,221.99	06/2019 09/2019	09/2021	27(O) 0	23/26
311	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND ,	10/2004	4,237.96 4,238.00	4,552.00	3,268.00	10/2017	-	-	0/0
312	PATRATU STPP-I (3X800MW) - [N18000275]NTPC,JHARKHAND ,	11/2017	18,668.00 -	18,668.00	2,004.32	03/2023 -	03/2023	0(O) -	1/1
313	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA , Central Sector Projects	05/2017	445.89 -	445.89	285.22	02/2019 -	03/2020	13(O) -	0/0
314	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH ,	03/2013	11,638.55 -	12,865.92	12,188.01	01/2018 03/2020	03/2020	26(O) 0	39/42
315	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC,MADHYA PRADESH ,	03/2015	9,870.51 -	11,148.86	8,619.60	01/2020 -	01/2020	0(O) -	34/40
316	AMELIA COAL MINE - [N18000252]THDCIL,MADHYA PRADESH , Central Sector Projects	01/2017	2,104.21 -	1,587.16	307.48	09/2020 -	09/2020	0(O) -	9/16
317	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA ,	03/2012	7,921.47 -	7,921.47	5,302.00	09/2016 -	-	-	41/41
318	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR ,	12/1999	578.62 -	578.62	.00	06/2006 -	-	-	0/0
319	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE ,	10/2008	4,824.12 -	5,071.94	4,565.74	10/2012 -	12/2019	86(O) -	8/11
320	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE ,	02/2009	11,130.19 -	14,719.10	12,814.08	08/2013 -	03/2022	103(O) -	23/26
321	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE ,	10/2011	487.49 -	639.46	564.32	06/2014 -	10/2019	64(O) -	10/12
322	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE ,	10/2013	1,364.52 -	1,891.41	1,263.11	04/2016 -	11/2019	43(O) -	8/12
323	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE ,	01/2014	374.63 -	374.63	213.02	04/2016 -	12/2019	44(O) -	0/0
324	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE ,	05/2014	522.29 -	546.36	466.42	11/2016 -	03/2020	40(O) -	8/12
325	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE ,	06/2014	5,151.37 -	5,151.37	3,153.93	03/2018 -	12/2019	21(O) -	9/12
326	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE ,	02/2014	196.58 -	225.28	164.27	02/2016 -	06/2019	-	16/17
327	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]PGCIL,MULTI STATE ,	01/2015	268.80 -	340.88	257.89	03/2018 -	06/2019	-	1/3
328	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE ,	01/2015	871.62 -	871.62	582.02	10/2017 -	11/2019	25(O) -	0/5

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
329	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE ,	01/2015	203.28 -	260.03	193.57	07/2017 -	10/2019	27(O) -	3/5
330	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE ,	03/2015	197.40 -	197.40	83.07	03/2018 -	12/2019	21(O) -	0/0
331	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE ,	03/2016	808.63 -	808.63	525.58	01/2018 -	03/2020	26(O) -	0/0
332	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE ,	05/2016	3,519.59 -	3,519.59	2,502.91	05/2019 -	12/2019	7(O) -	0/0
333	HVDC BIPOLE LINK BETWEEN WR (RAIGARH CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE ,	05/2016	14,733.37 -	14,733.37	8,796.37	11/2019 -	11/2019	0(O) -	0/0
334	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE ,	09/2016	562.25 -	562.25	414.25	03/2019 -	11/2019	8(O) -	0/0
335	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]PGCIL,MULTI STATE ,	03/2017	251.60 -	251.60	191.96	06/2019 -	06/2019	-	0/0
336	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE ,	03/2017	283.72 -	283.72	193.70	11/2019 -	11/2019	0(O) -	0/0
337	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE ,	10/2016	408.46 -	408.46	288.56	01/2019 -	12/2019	11(O) -	0/0
338	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE ,	10/2016	608.24 -	608.24	413.61	04/2019 -	11/2019	7(O) -	0/0
339	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]PGCIL,MULTI STATE ,	02/2017	195.05 -	195.05	120.83	02/2020 -	02/2020	0(O) -	0/0
340	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE ,	02/2017	322.30 -	322.30	158.10	02/2019 -	12/2019	10(O) -	0/0
341	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE ,	02/2017	235.53 -	235.53	124.27	06/2019 -	03/2020	9(O) -	0/0
342	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE ,	03/2017	379.95 -	379.95	76.66	12/2019 -	12/2019	0(O) -	0/0
343	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH CHATTISGARH) AND SOUTHERN REGION (PUGALAR TM) NOR - [N18000247]PGCIL,MULTI STATE ,	02/2017	5,070.13 -	5,070.13	2,771.21	04/2020 -	04/2020	0(O) -	0/0
344	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE ,	03/2017	337.75 -	337.75	92.75	06/2019 -	12/2019	6(O) -	0/0
345	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE ,	12/2014	4,754.42 -	9,072.36	1,301.58	12/2018 -	12/2020	24(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
346	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE ,	12/2014	5,111.33 -	6,880.36	1,641.35	12/2018 -	12/2020	24(O) -	0/0
347	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE , Central Sector Projects	12/2015	3,654.00 -	3,654.00	3,427.57	04/2019 -	11/2019	7(O) -	0/0
348	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE , Central Sector Projects	03/2017	3,500.00 3,500.00	3,500.00	1,758.00	07/2020 -	07/2020	0(O) -	0/0
349	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE , Central Sector Projects	08/2017	1,931.39 -	1,931.39	1,054.28	02/2020 -	02/2020	0(O) -	0/0
350	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE ,	09/2017	198.49 -	198.49	83.31	09/2019 -	02/2020	5(O) -	0/0
351	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE ,	11/2017	358.83 -	358.83	121.83	05/2020 -	05/2020	0(O) -	0/0
352	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA ,	02/2014	12,532.44 -	13,740.53	9,726.03	12/2018 02/2020	09/2020	21(O) 0	34/38
353	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA ,	04/2016	844.64 -	844.64	435.06	04/2019 -	11/2019	7(O) -	0/0
354	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC,ODISHA ,	05/2016	1,885.13 -	1,885.13	527.90	12/2018 -	03/2020	15(O) -	0/0
355	TRAMMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL,RAJASTHAN ,	07/2016	1,429.38 -	1,429.38	1,045.19	01/2019 07/2019	09/2019	8(O) 0	0/0
356	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU ,	05/2005	1,779.29 -	2,187.32	2,237.45	11/2008 -	-	-	20/22
357	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU , Central Sector Projects	05/2017	186.17 -	186.17	107.75	07/2019 -	12/2019	5(O) -	0/0
358	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA ,	01/2016	10,598.98 -	10,598.98	5,557.96	11/2020 06/2021	06/2021	7(O) 0	24/24
359	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH ,	09/2014	9,188.98 -	9,188.98	6,502.04	07/2019 03/2020	07/2020	12(O) 1	34/35
360	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH ,	05/2011	195.42 -	294.60	310.08	02/2014 -	12/2019	70(O) -	7/8
361	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH , Joint Venture	04/2012	9,750.89 -	12,176.28	9,794.00	02/2017 06/2020	06/2020	40(O) 0	34/40
362	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH ,	03/2019	11,089.42 -	11,089.42	521.82	09/2023 -	09/2023	0(O) -	0/0
363	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000273]NTPC,UTTAR PRADESH ,	12/2018	587.44 -	587.44	250.00	09/2020 -	09/2020	0(O) -	0/0
364	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000274]NTPC,UTTAR PRADESH ,	03/2019	349.00 -	349.00	125.00	11/2020 -	11/2020	0(O) -	0/0
365	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND ,	07/2006	1,657.00 -	5,024.35	3,047.08	02/2016 -	06/2022	76(O) -	17/30
366	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND ,	11/2006	2,978.48 5,867.38	5,867.38	4,182.37	03/2013 12/2020	01/2021	94(O) 1	6/15

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
367	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND ,	08/2008	2,491.58 -	4,397.80	1,770.91	06/2013 -	12/2022	114(O) -	10/13
368	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND ,	07/2012	1,527.00 -	1,801.07	148.93	08/2017 -	-	-	0/15
369	NAITWAR MORI HEP - [N18000265]SJVN,UTTARAKHAND ,	10/2017	648.33 -	648.33	265.90	12/2021 -	12/2021	0(O) -	4/32
370	RAMMAM-III HEP (3X40 MW) - [N18000178]NTPC,WEST BENGAL ,	09/2014	1,381.84 -	1,592.34	486.24	09/2019 02/2022	02/2022	29(O) 0	5/9
371	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL ,	04/2016	454.11 -	454.11	291.64	04/2018 -	01/2020	21(O) -	0/0
372	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC,WEST BENGAL ,	12/2016	529.68 -	529.68	140.10	11/2018 -	03/2020	16(O) -	0/0
	Total		2,85,786.68 -	3,59,673.67	2,19,075.70				595/783
	<u>HEAVY INDUSTRY</u>								
373	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL,DELHI , Central Sector Projects	08/2016	1,554.00 -	1,554.00	335.03	09/2019 -	09/2019	0(O) -	0/0
	Total		1,554.00 -	1,554.00	335.03				0/0
	<u>HEALTH AND FAMILY WELFARE</u>								
374	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS-MNAGLAGIRI GUNTUR ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH , Central Sector Projects	08/2017	272.19 -	272.19	140.58	03/2019 -	10/2019	7(O) -	0/0
375	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH , Central Sector Projects	03/2018	601.02 -	601.02	85.04	- -	02/2020	- -	0/0
376	LGBRIMH-TEZPUR ASSAM - [N21000007]HSCC,ASSAM ,	07/2012	175.57 -	175.57	113.50	12/2014 -	-	-	0/0
377	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI ASSAM - [N21000027]HITES,ASSAM ,	05/2017	875.00 -	875.00	39.27	05/2021 -	10/2021	5(O) -	0/0
378	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI ,	02/2013	414.11 -	513.89	147.00	11/2013 -	10/2020	83(O) -	0/0
379	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI ,	12/2013	204.44 -	204.44	188.00	05/2017 -	09/2019	28(O) -	2/2
380	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI ,	08/2014	293.65 -	293.65	290.71	05/2017 -	-	-	3/5
381	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI ,	12/2017	156.56 -	156.65	54.94	- -	02/2020	- -	0/0
382	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA , Central Sector Projects	01/2018	249.01 -	249.01	73.40	- -	05/2020	- -	0/0
383	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA ,	09/2014	505.58 -	523.00	508.29	03/2018 -	-	-	1/2
384	AIIMS BILASPUR - [N21000028]NBCC,HIMACHAL PRADESH ,	04/2018	1,351.00 -	1,351.00	137.87	09/2021 -	09/2021	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
385	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA , Central Sector Projects	08/2017	274.19 -	274.19	169.93	03/2019 -	10/2019	7(O) -	0/0
386	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA , Central Sector Projects	03/2018	582.99 -	582.99	112.97	- -	02/2020	- -	0/0
387	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA ,	10/2016	363.99 -	363.99	166.19	05/2018 -	09/2019	16(O) -	0/0
388	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB ,	07/2016	152.95 -	152.95	118.23	02/2018 -	09/2019	19(O) -	1/1
389	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA PUNJAB - [N21000026]HITES,PUNJAB ,	07/2016	703.00 -	703.00	184.93	06/2020 -	08/2020	2(O) -	0/0
390	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH , Central Sector Projects	03/2018	268.84 -	268.84	99.26	- -	04/2020	- -	0/0
391	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH ,	07/2016	785.00 -	785.00	244.66	04/2020 -	06/2020	2(O) -	0/0
392	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL ,	08/2016	244.00 -	244.00	241.39	09/2018 -	-	-	0/0
393	RESIDENTIALCOMPLEX AND OPD BLOCK AIIMS KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL , Central Sector Projects	08/2017	355.15 -	355.15	148.84	03/2019 -	03/2020	12(O) -	0/0
394	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC,WEST BENGAL , Central Sector Projects	04/2018	651.99 -	651.99	112.82	- -	02/2020	- -	0/0
	Total		9,480.23 -	9,597.52	3,377.82				7/10
	<u>RAILWAYS</u>								
395	NANDYAL-YERRAGUNTALA(NL) SCR - [220100192]SCR,ANDHRA PRADESH ,	03/1996	164.36 -	1,050.00	999.64	02/2009 -	-	-	0/0
396	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH ,	12/2001	1,045.20 -	2,120.16	412.87	03/2009 -	03/2023	168(O) -	0/0
397	GUDUR-DURGARAJPATNAM - [N22000265]SCR,ANDHRA PRADESH ,	04/2011	761.37 -	761.37	.52	- -	-	-	0/0
398	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH ,	04/2013	829.00 -	1,599.39	.94	- -	-	-	1/1
399	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH ,	04/2011	2,288.70 -	2,288.70	667.03	03/2021 -	03/2024	36(O) -	0/1
400	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH ,	03/2012	1,503.71 -	1,503.71	1,563.45	03/2020 -	03/2022	24(O) -	0/0
401	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH ,	04/2015	3,873.07 -	3,873.07	.38	- -	-	-	0/0
402	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH ,	04/2016	3,631.00 -	3,631.00	407.42	03/2022 -	03/2023	12(O) -	0/0
403	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH ,	04/2015	3,246.26 -	3,548.67	1,072.89	12/2023 -	12/2023	0(O) -	0/0
404	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]JECOR,ANDHRA PRADESH ,	04/2015	2,499.71 -	3,382.95	373.22	03/2022 -	03/2022	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
405	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH ,	01/2013	387.70 -	387.70	323.91	03/2018 -	-	-	0/0
406	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH ,	08/2016	234.50 -	235.00	11.11	03/2019 -	12/2020	21(O) -	0/0
407	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT) NEFR - [N22000086]NFR,ASSAM ,	09/2006	385.20 1,532.00	1,532.00	629.19	03/2019 -	03/2020	12(O) -	0/0
408	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM ,	04/2011	314.00 728.00	728.00	704.09	03/2019 -	03/2020	12(O) -	0/0
409	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM ,	04/2015	2,232.32 -	2,182.00	654.38	03/2022 -	03/2020	-24(O) -	0/0
410	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM ,	04/2015	870.96 -	2,136.01	502.44	03/2021 -	03/2021	0(O) -	0/0
411	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC) ECR - [220100240]ECR,BIHAR ,	04/1997	324.73 898.53	1,050.00	1,040.00	03/2012 -	03/2020	96(O) -	0/0
412	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR ,	04/1997	162.87 614.45	614.45	305.83	- -	03/2022	- -	0/0
413	HAJIPUR-SUGAULI VIA VAISHALI (NL) ECR - [220100303]ECR,BIHAR ,	04/2003	528.65 2,066.78	2,066.78	1,436.88	- -	03/2023	- -	0/0
414	KOSI BRIDGE (NL) ECR - [220100304]ECR,BIHAR ,	04/2002	499.41 516.02	516.02	397.11	03/2020 -	03/2020	0(O) -	0/0
415	DANIAWAN-BIHARSARIF (NL) ECR - [220100311]ECR,BIHAR ,	04/2001	406.92 -	339.00	200.00	- -	-	-	0/0
416	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR ,	04/1996	477.88 751.55	751.55	673.69	03/2012 -	03/2020	96(O) -	0/0
417	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) NEFR - [N22000087]NFR,BIHAR ,	09/2006	532.87 2,145.00	2,145.00	932.80	03/2019 -	03/2020	12(O) -	0/0
418	KISHANGANJ JALALGARH NL NEFR - [N22000101]NFR,BIHAR ,	04/2008	333.76 -	360.00	6.67	- 03/2022	03/2022	- 0	0/0
419	ARA-BHABHUA ROAD (NL) - [N22000166]ECR,BIHAR ,	04/2008	633.87 -	633.87	.40	- -	03/2023	- -	0/0
420	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR ,	04/2008	620.57 -	620.57	.28	- -	03/2024	- -	0/0
421	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR ,	04/2008	445.25 -	445.25	1.14	- -	03/2024	- -	0/0
422	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR ,	04/2008	326.20 -	2,995.01	1.94	- -	03/2024	- -	0/0
423	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR ,	04/1999	325.00 735.20	735.20	362.10	- -	03/2021	- -	0/0
424	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR ,	04/2006	378.56 -	2,609.00	376.63	- -	03/2022	- -	0/0
425	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR ,	04/2005	205.00 -	205.00	5.21	- -	03/2024	- -	0/0
426	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR ,	04/2006	211.00 -	1,006.00	24.16	- -	03/2024	- -	0/0
427	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR ,	04/2008	678.62 -	678.62	17.20	- -	03/2024	- -	0/0
428	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR ,	04/2008	228.05 -	228.05	1.53	- -	03/2024	- -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
429	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR ,	04/2008	1,605.17 1,605.17	1,605.17	23.49	- 03/2023	03/2023	- 0	0/0
430	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR ,	04/2008	192.56 -	192.56	.39	- -	03/2024	- -	0/0
431	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR ,	04/2008	281.30 -	281.30	.60	- -	03/2024	- -	0/0
432	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR ,	04/2004	372.14 1,470.50	1,470.50	777.71	- -	03/2021	- -	0/0
433	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR ,	04/2009	548.00 -	819.01	489.11	03/2020 -	03/2022	24(O) -	0/0
434	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR ,	04/2013	213.01 367.17	425.17	406.05	- -	01/2020	- -	0/0
435	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR ,	05/2015	380.00 519.33	519.33	143.36	- -	02/2023	- -	0/0
436	CONSTRUCTION OF ROBS IN THE STATE OF BIHAR (NEW ROBS-12) - [N22000337]SER,BIHAR ,	08/2010	400.00 -	400.00	.00	03/2014 -	-	-	0/0
437	CONSTRUCTION OF ROBS IN THE STATE OF BIHAR - [N22000344]ECR,BIHAR ,	07/2004	599.63 674.00	674.00	.00	12/2007 -	-	-	0/0
438	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR ,	12/2015	1,200.20 1,200.20	1,200.20	397.14	03/2020 -	10/2021	19(O) -	0/1
439	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR ,	12/2015	1,491.47 -	1,491.47	438.38	03/2020 -	12/2022	33(O) -	1/1
440	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR ,	01/1991	332.15 546.71	546.71	541.07	07/2014 -	-	-	0/0
441	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR ,	04/2016	744.04 1,215.54	1,215.54	63.74	03/2021 -	03/2022	12(O) -	0/0
442	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR ,	04/2016	731.64 1,185.73	1,185.73	32.31	03/2021 -	03/2022	12(O) -	0/0
443	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR,BIHAR ,	04/1998	180.82 726.31	726.31	502.13	- -	10/2019	- -	0/0
444	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA DANIYAWAN-BIHARSHARIF - [N22000476]ECR,BIHAR ,	04/1991	329.39 803.11	1,483.14	1,029.84	- -	12/2021	- -	0/0
445	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH ,	12/2012	1,160.00 -	1,160.83	682.29	03/2020 -	03/2023	36(O) -	1/1
446	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH ,	03/2007	1,402.02 -	1,100.00	1,050.36	03/2020 -	06/2020	3(O) -	0/0
447	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH ,	05/2014	207.00 -	207.00	153.83	03/2018 -	-	-	0/0
448	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR,CHHATISGARH ,	04/2008	872.00 1,226.51	1,226.51	1,044.67	12/2019 10/2019	10/2019	-2(O) 0	0/0
449	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATISGARH ,	04/2015	1,973.00 1,973.66	1,973.66	139.42	03/2021 12/2022	12/2022	21(O) 12	0/1
450	GEVRA ROAD PENDRA ROAD - [N22000488]IRCON,CHHATISGARH ,	02/2014	2,288.00 -	4,970.11	619.50	03/2022 -	12/2022	9(O) -	0/1
451	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON,CHHATISGARH ,	04/2013	3,055.00 -	3,055.00	1,729.64	09/2018 -	12/2020	27(O) -	0/1

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
452	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498]RITES,CHHATISGARH ,	02/2016	393.98 -	393.98	241.23	03/2020 -	03/2020	0(O) -	0/0
453	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI ,	04/1999	156.65 -	197.17	107.86	- -	03/2024	- -	0/0
454	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI ,	04/2012	295.68 -	295.68	79.53	- -	03/2023	- -	0/0
455	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT ,	04/2008	829.74 1,215.34	1,310.23	1,394.73	03/2020 03/2021	03/2021	12(O) 0	0/0
456	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT ,	04/2008	318.24 321.62	321.62	125.76	03/2012 03/2022	03/2022	120(O) 0	0/0
457	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT ,	04/2006	117.36 196.95	202.35	809.40	03/2011 03/2017	03/2017	-	0/0
458	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT ,	04/2012	975.62 -	1,082.32	994.30	12/2021 -	12/2021	0(O) -	0/0
459	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT ,	04/2012	644.38 -	644.38	352.02	03/2021 -	03/2021	0(O) -	0/0
460	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT ,	04/2011	844.10 844.10	844.10	97.74	- 03/2021	03/2021	- 0	0/0
461	RAJKOT-VERAVAL WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT ,	04/1994	320.66 858.56	858.96	534.00	03/2019 03/2022	03/2022	36(O) 0	0/0
462	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT ,	04/2013	1,548.66 -	1,548.66	1,268.31	12/2021 -	03/2022	3(O) -	0/0
463	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT ,	04/2011	1,037.15 1,037.15	1,037.15	992.18	03/2021 03/2022	03/2022	12(O) 0	0/0
464	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT ,	04/2015	1,002.39 1,002.39	1,002.39	378.38	03/2021 03/2021	03/2021	0(O) 0	0/0
465	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT ,	10/2013	343.00 -	343.00	222.83	03/2019 -	12/2019	9(O) -	0/0
466	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT ,	03/2017	243.60 -	243.60	.00	- -	-	-	0/0
467	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT ,	03/2012	248.26 -	248.26	.00	- -	-	-	0/0
468	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT ,	03/2012	153.83 -	153.83	.00	- -	-	-	0/0
469	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT ,	02/1991	551.51 809.07	809.07	616.90	03/2019 03/2020	03/2020	12(O) 0	0/0
470	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT ,	04/2017	691.84 663.29	663.29	166.84	03/2020 03/2021	03/2021	12(O) 0	0/0
471	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA ,	04/2012	287.00 -	694.00	220.42	12/2011 -	03/2021	111(O) -	0/0
472	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA ,	12/2015	346.32 -	346.32	286.78	03/2019 -	03/2020	12(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
473	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH ,	04/2008	2,966.99 -	7,000.00	398.76	12/2026 -	12/2025	-12(O) -	0/0
474	UDHAMPUR-SRINAGAR-BARAMULLA (NL) NR - [220100133]NR,JAMMU AND KASHMIR ,	03/1995	2,500.00 27,949.00	27,949.00	19,403.28	11/2002 -	06/2022	235(O) -	0/0
475	KODERMA-RANCHI VIA BARKAKANA (NL) ECR - [220100222]ECR,JHARKHAND ,	03/1999	1,033.07 3,020.95	3,376.00	3,307.82	- -	03/2021	- -	0/0
476	KODERMA-TILAIYA (NL) ECR - [220100305]ECR,JHARKHAND ,	04/2002	459.91 1,625.87	1,625.87	508.33	- -	03/2021	- -	0/0
477	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND ,	04/2012	258.20 358.68	358.68	258.09	12/2018 12/2018	06/2020	18(O) 0	0/0
478	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND ,	04/2012	148.77 -	377.00	180.95	12/2016 08/2018	12/2019	36(O) 1	0/0
479	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND ,	03/2016	1,724.20 -	1,993.24	384.82	03/2021 -	12/2021	9(O) -	0/0
480	GARHWA ROAD-RAMNA - [N22000465]ECR,JHARKHAND ,	03/2015	348.23 -	348.23	177.12	03/2021 -	12/2020	-3(O) -	0/0
481	HUBLI-ANKOLA(NL) SWR - [220100193]SWR,KARNATAKA ,	04/1997	2,315.00 -	2,135.00	144.76	- -	12/2024	- -	0/0
482	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA ,	04/1996	1,382.78 -	1,382.78	7.35	03/2002 -	03/2024	264(O) -	0/0
483	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA ,	04/2011	1,801.01 -	1,801.01	44.36	- -	12/2023	- -	0/0
484	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA ,	04/2010	986.30 -	986.30	297.70	03/2016 -	12/2023	93(O) -	0/1
485	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA ,	04/2013	558.00 -	692.43	.00	- -	12/2023	- -	0/0
486	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA ,	04/2011	832.47 -	832.47	.94	03/2016 -	03/2024	96(O) -	0/0
487	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA ,	04/2011	348.85 -	348.85	.35	- -	12/2023	- -	0/0
488	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA ,	04/2010	2,127.00 -	2,900.00	1,660.87	03/2023 -	03/2024	12(O) -	0/1
489	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA ,	04/2011	146.75 -	167.50	.34	- -	12/2023	- -	0/0
490	GADAG-WADI NL - [N22000299]SWR,KARNATAKA ,	04/2013	2,841.84 -	2,841.84	113.63	12/2018 -	12/2024	72(O) -	0/0
491	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA ,	04/2013	327.25 -	367.77	.00	- -	12/2023	- -	0/0
492	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA ,	04/2012	279.54 -	279.54	28.51	03/2016 -	12/2023	93(O) -	0/0
493	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA ,	03/2015	1,156.94 -	1,140.93	786.13	03/2020 -	03/2021	12(O) -	0/5
494	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA ,	03/2015	578.00 -	578.00	509.07	03/2020 -	03/2020	0(O) -	0/2
495	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA ,	03/1996	644.78 -	889.52	438.39	03/2017 -	03/2020	36(O) -	0/0
496	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA ,	10/1998	1,566.00 2,815.62	2,815.62	264.28	- -	-	-	0/0
497	KUMBALAM-TURAVUR - [N22000191]SR,KERALA ,	04/2011	252.96 252.96	252.96	8.50	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
498	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA ,	04/2010	189.24 189.24	189.24	6.72	- -	- -	- -	0/0
499	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA ,	02/2015	1,431.90 1,431.90	1,431.90	75.00	- 06/2022	- -	- -	0/0
500	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA ,	02/2015	1,000.00 828.50	828.50	.08	- -	- -	- -	0/0
501	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA ,	02/2012	550.00 -	550.00	.00	03/2016 -	- -	- -	0/0
502	RAMGANJMUHDI-BHOPAL (NL) WCR - [220100314]WCR,MADHYA PRADESH ,	04/2001	424.60 -	2,909.99	1,926.25	03/2021 -	03/2023	24(O) -	0/14
503	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH ,	04/2005	383.79 -	1,413.76	1,324.64	- -	10/2019	- -	0/0
504	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH ,	04/2008	3,503.69 3,860.00	3,860.40	1,676.43	03/2022 03/2023	03/2023	12(O) 0	0/0
505	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH ,	12/2015	1,763.93 -	1,763.93	624.49	03/2020 -	03/2022	24(O) -	1/1
506	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH ,	04/2011	1,485.85 -	1,485.85	1,074.88	12/2020 -	03/2021	3(O) -	0/0
507	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH ,	06/2016	2,478.23 -	2,478.23	367.59	03/2022 -	03/2023	12(O) -	0/10
508	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH ,	08/2016	582.13 -	1,247.64	154.63	03/2022 -	09/2022	6(O) -	0/1
509	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH ,	12/2015	174.00 -	174.00	151.24	03/2019 -	02/2020	11(O) -	0/0
510	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH ,	04/2010	585.93 737.72	1,300.44	646.30	02/2019 03/2020	06/2020	16(O) 0	0/1
511	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH ,	04/2015	1,370.00 1,370.00	1,370.00	281.19	12/2021 12/2021	12/2021	0(O) 0	0/0
512	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH ,	04/2016	700.00 603.69	603.69	92.30	06/2020 06/2021	06/2021	12(O) 0	0/0
513	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA ,	03/1996	495.44 1,781.98	2,980.41	1,417.63	03/2004 -	03/2021	204(O) -	0/0
514	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]CR,MAHARASHTRA ,	02/1997	2,271.50 -	3,712.50	2,380.30	03/2021 -	03/2022	12(O) -	0/0
515	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA ,	04/2008	5,300.00 918.53	918.53	284.75	03/2014 03/2021	03/2021	84(O) 0	0/0
516	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA ,	04/2012	714.10 -	714.10	65.20	04/2016 -	-	-	0/0
517	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA ,	04/2008	3,168.29 -	3,168.29	1,202.43	03/2023 -	03/2023	0(O) -	0/0
518	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA ,	04/2011	792.89 -	1,377.48	308.67	03/2021 -	03/2022	12(O) -	0/0
519	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA ,	04/2011	184.06 199.12	305.00	269.39	03/2019 12/2019	12/2019	9(O) 0	0/0
520	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA ,	04/2012	540.02 -	540.02	235.70	03/2022 -	03/2024	24(O) -	0/0
521	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA ,	02/2016	9,968.00 -	9,968.00	.00	03/2024 -	03/2024	0(O) -	0/0
522	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA ,	02/2016	2,425.00 -	5,341.68	.00	03/2024 -	03/2024	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
523	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA ,	02/2016	2,750.00 -	3,438.51	.00	03/2024 -	03/2024	0(O) -	0/0
524	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA ,	02/2015	1,272.19 -	1,272.19	296.03	03/2022 -	03/2023	12(O) -	0/0
525	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA ,	02/2015	2,449.91 -	2,449.91	165.28	03/2023 -	03/2023	0(O) -	0/0
526	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA ,	02/2015	3,627.47 3,627.00	3,627.47	686.42	03/2024 -	03/2022	-24(O) -	0/0
527	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA ,	02/2016	1,876.00 -	2,081.27	121.17	03/2023 -	03/2023	0(O) -	0/0
528	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA ,	02/2016	1,035.16 -	1,035.16	90.49	03/2022 -	03/2024	24(O) -	0/0
529	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA ,	02/2016	637.95 -	637.95	58.36	03/2023 -	03/2024	12(O) -	0/0
530	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA ,	03/2009	713.48 -	1,950.00	1,957.22	03/2020 -	03/2020	0(O) -	0/0
531	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA ,	04/2015	723.78 -	723.78	.19	12/2025 -	03/2025	-9(O) -	0/0
532	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA ,	09/2016	1,908.51 2,686.63	2,686.63	443.56	03/2023 03/2023	03/2023	0(O) 0	0/1
533	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA ,	10/2013	305.00 -	305.00	261.28	03/2019 -	12/2019	9(O) -	0/0
534	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA ,	03/2010	265.88 -	265.88	.00	- -	-	-	0/0
535	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA ,	03/2012	217.38 -	217.38	.00	- -	-	-	0/0
536	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA ,	06/2018	229.00 403.00	860.92	39.69	12/2021 03/2023	03/2023	15(O) 0	0/1
537	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR ,	04/2003	4,454.17 13,809.00	12,524.00	9,123.93	03/2011 -	03/2020	108(O) -	0/0
538	NEW BG LINE FROM BYRNIAH TO SHILLONG - [N22000205]NFR,MEGHALAYA ,	04/2010	906.46 -	6,000.00	261.76	03/2021 -	03/2021	0(O) -	0/0
539	BHAIRABI SAIRONG NL NEFR - [N22000100]NFR,MIZORAM ,	04/2008	2,393.47 4,968.00	5,021.45	3,075.08	03/2014 03/2022	03/2022	96(O) 0	0/0
540	GONDIA-JABALPUR(GC) (SECR) - [220100186]SECR,MULTI STATE ,	02/1997	511.86 1,756.92	1,756.92	1,661.79	04/2020 12/2020	12/2020	8(O) 0	0/1
541	NANGALDAM-TALWARA(NL) NR - [220100188]NR,MULTI STATE ,	03/1981	450.00 -	2,010.00	654.07	07/2012 -	03/2024	140(O) -	0/0
542	MUNEERABAD-MAHABOONNAGAR(NL) SCR - [220100205]SCR,MULTI STATE ,	04/1997	1,723.00 1.00	1,723.00	1,368.46	03/2000 -	03/2021	252(O) -	0/0
543	LALITPUR-SATNA-REWA-SINGRULI NL (NCR) - [220100232]WCR,MULTI STATE ,	09/1998	247.66 -	6,093.31	1,835.18	05/2008 -	03/2023	178(O) -	0/9
544	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) NEFR - [220100266]NFR,MULTI STATE ,	04/2000	1,180.19 3,300.00	4,541.00	3,279.71	12/2008 -	03/2021	147(O) -	0/0
545	DEOGHAR - SULTANGANJ (NL) ER - [220100273]ER,MULTI STATE ,	04/2000	607.09 -	1,425.44	637.42	02/2013 -	03/2024	133(O) -	0/0
546	HATHUA-BHATNI (NL) (NER) - [220100319]NER,MULTI STATE ,	04/2005	230.03 -	230.03	277.14	12/2022 -	12/2022	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
547	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE ,	03/2007	243.78 -	895.00	106.55	12/2021 -	12/2021	0(O) -	0/0
548	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE ,	03/2013	295.00 -	477.31	328.19	01/2019 -	01/2020	12(O) -	0/0
549	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE ,	04/2007	1,347.26 1,347.26	1,347.26	724.63	03/2022 03/2022	03/2022	0(O) 0	0/0
550	DAHOD-INDORE VIA SARDARPUR JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE ,	04/2007	1,640.04 1,640.04	1,640.04	682.91	03/2022 03/2023	03/2023	12(O) 0	0/0
551	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE ,	04/2011	2,082.75 -	4,079.15	185.11	- -	-	-	0/1
552	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE ,	04/2011	2,912.96 -	3,845.60	137.90	03/2022 -	12/2024	33(O) -	0/3
553	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE ,	04/2010	2,030.50 -	2,030.50	19.07	- -	-	-	0/0
554	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE ,	04/2010	651.00 -	1,009.00	7.96	03/2015 -	-	-	0/0
555	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE ,	04/2008	415.67 -	549.75	15.54	- -	03/2024	- -	0/0
556	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE ,	04/2013	1,798.00 -	2,496.67	.00	03/2019 -	-	-	0/0
557	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE ,	04/2008	523.52 -	2,300.00	2.28	- -	-	-	0/0
558	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE ,	04/2007	270.14 457.08	457.08	373.51	- -	-	-	0/0
559	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE ,	04/2010	242.22 -	471.00	68.15	03/2020 -	03/2020	0(O) -	0/0
560	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE ,	04/2010	241.52 -	394.28	272.88	- -	03/2021	-	0/0
561	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE ,	04/2011	414.84 -	661.00	122.05	03/2020 -	03/2020	0(O) -	0/0
562	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE ,	04/1999	819.23 -	1,871.00	1,082.01	- -	-	-	0/0
563	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE ,	04/2011	120.70 -	1,800.00	170.47	03/2019 -	12/2019	9(O) -	0/0
564	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE ,	04/1987	406.99 -	545.70	148.43	03/2006 -	03/2025	228(O) -	0/0
565	SULTANGANJ-KATURIA VIA ASARGANJ TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE ,	04/2007	450.00 -	1,261.34	.00	- -	03/2025	- -	0/0
566	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE ,	04/2010	172.03 -	260.10	10.73	- -	03/2025	- -	0/0
567	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE ,	04/2013	915.98 -	2,137.81	294.91	03/2022 -	03/2025	36(O) -	0/0
568	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE ,	04/2011	288.35 -	382.90	382.90	- -	03/2020	- -	0/0
569	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE ,	04/2011	261.38 -	471.81	467.50	- -	05/2019	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
570	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE ,	04/2001	923.52 -	995.10	448.78	03/2016 -	03/2025	108(O) -	0/0
571	CHINPAI-SAINTHIA DOUBLING MM FOR PRANTI-SURI CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE ,	04/2005	595.51 -	769.40	102.47	03/2017 -	03/2025	96(O) -	0/0
572	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE ,	04/2010	174.56 -	174.56	71.42	- -	03/2025	- -	0/0
573	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE ,	04/2010	277.28 -	266.32	160.40	03/2016 -	03/2025	108(O) -	0/0
574	DANKUNI-CHANDANPUR 4TH LINE 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE ,	04/2010	365.17 -	296.43	234.43	03/2017 -	03/2025	96(O) -	0/0
575	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE ,	04/2010	157.94 -	157.94	51.75	11/2018 -	03/2021	28(O) -	0/0
576	BARIARPIUR-MANANPURVIA KHARAGPUER LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE ,	04/2007	450.55 -	250.55	20.12	- -	03/2025	- -	0/0
577	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE ,	04/2010	365.17 -	527.54	1.76	- -	03/2025	- -	0/0
578	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE ,	04/2011	542.18 -	693.80	443.81	03/2020 -	03/2021	12(O) -	0/0
579	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE ,	04/2011	175.80 -	245.41	245.41	- -	03/2021	- -	0/0
580	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE ,	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	108(O) -	0/0
581	NEW ALIPUR TO AKRA MM FOR BUDGE BUDGE-PUJALI NL PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE ,	04/2010	494.54 -	494.59	32.00	03/2005 -	03/2025	240(O) -	0/0
582	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE ,	04/2000	297.47 -	298.22	52.09	- -	03/2025	- -	0/0
583	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE ,	04/2003	337.96 -	336.96	70.20	- -	03/2025	- -	0/0
584	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE ,	04/2009	499.96 -	680.68	158.60	02/2012 -	03/2025	157(O) -	0/0
585	LILUAH-DANKUNI 3RD LINE MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE ,	04/2009	257.42 -	257.42	106.51	03/2014 -	03/2025	132(O) -	0/0
586	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE ,	04/2011	166.89 -	166.89	.02	- -	03/2025	- -	0/0
587	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE ,	04/2012	1,856.95 -	2,200.00	252.81	03/2023 -	03/2024	12(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
588	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE ,	04/2012	923.23 -	1,787.00	2.46	-	-	-	1/1
589	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE ,	04/2007	336.91 -	800.00	512.67	-	03/2022	-	0/0
590	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE ,	04/2013	296.00 -	466.65	.00	-	12/2023	-	0/0
591	RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE ,	04/2007	2,062.30 -	2,062.20	825.58	-	03/2022	-	0/2
592	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE ,	04/2010	704.31 -	1,352.74	269.07	03/2020	03/2020	0(O)	1/1
593	KADAPA-BANGALORE (NL) KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE ,	04/2008	2,132.77 -	2,132.77	331.17	03/2014	03/2024	120(O)	1/1
594	MONIGRAM- NIMITITA - [N22000301]ER,MULTI STATE ,	04/2012	250.93 -	310.70	263.08	-	03/2024	-	0/0
595	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE ,	05/2015	600.00 -	685.99	47.07	03/2020	04/2022	25(O)	0/0
596	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE ,	05/2015	860.43 -	860.43	697.21	03/2020	03/2020	0(O)	0/0
597	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE ,	03/2015	1,614.59 -	1,870.41	914.00	03/2019	03/2021	24(O)	0/0
598	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE ,	05/2015	678.54 678.54	678.54	492.44	03/2019	02/2021	23(O)	0/38
599	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE , Central Sector Projects	10/2006	11,589.00 30,357.00	28,181.00	.00	-	-	-	0/0
600	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE ,	04/2015	2,063.03 -	2,063.03	675.97	03/2021	03/2023	24(O)	0/0
601	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE ,	04/2015	636.38 -	636.38	.00	-	-	-	0/0
602	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE ,	12/2015	1,08,000.00 -	1,08,000.00	4,886.79	12/2023 12/2023	12/2023	0(O) 0	0/0
603	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE ,	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020	03/2020	0(O)	0/0
604	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE ,	04/2007	328.14 -	1,540.00	233.84	03/2023	03/2023	0(O)	0/0
605	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE ,	03/2002	625.00 -	845.58	834.59	03/2016	03/2021	60(O)	0/0
606	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND ,	04/2006	2,326.52 -	4,600.00	781.71	03/2015	10/2021	79(O)	0/0
607	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND ,	04/2013	4,274.00 -	4,274.00	.00	03/2020	03/2020	0(O)	0/0
608	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA ,	04/1994	2,923.13 -	3,791.66	1,237.04	03/2009	06/2024	183(O)	0/0
609	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA ,	04/1996	1,185.64 -	1,844.47	1,783.59	12/2017	03/2020	27(O)	0/0
610	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA ,	04/1998	1,202.70 -	1,202.70	914.39	02/2015	12/2021	82(O)	0/0
611	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA ,	04/2000	133.41 207.00	385.00	386.30	03/2009 03/2009	12/2019	129(O) 0	1/1

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
612	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA ,	04/2005	810.78 -	1,928.07	691.04	06/2021 -	06/2024	36(O) -	0/0
613	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA ,	04/2010	149.90 -	230.00	54.46	03/2015 -	-	-	0/0
614	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA ,	03/2011	1,111.99 -	1,539.28	924.93	02/2019 -	03/2022	37(O) -	0/0
615	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA ,	03/2013	843.04 -	843.04	133.25	10/2020 03/2023	03/2023	29(O) 0	0/0
616	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA ,	03/2012	155.81 -	238.03	226.50	03/2020 -	03/2021	12(O) -	0/0
617	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA ,	04/2015	1,547.38 -	1,547.38	346.97	03/2022 -	03/2023	12(O) -	0/0
618	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA ,	04/2015	2,361.74 -	2,361.74	162.82	03/2022 -	03/2025	36(O) -	0/0
619	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA ,	04/2015	701.61 -	810.02	122.59	11/2018 -	03/2022	40(O) -	0/0
620	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA ,	04/2015	1,172.92 -	1,172.92	397.91	12/2018 03/2022	03/2022	39(O) 0	0/0
621	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA ,	11/2015	969.83 1,312.96	1,312.96	549.97	03/2020 -	06/2020	3(O) -	0/0
622	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA ,	01/1991	2,335.67 -	2,335.68	598.12	12/2024 -	12/2024	0(O) -	0/0
623	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA ,	03/2006	948.04 -	1,500.00	1,323.18	03/2020 -	03/2021	12(O) -	0/0
624	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA ,	03/2009	942.95 -	1,120.00	1,010.21	03/2019 -	06/2022	39(O) -	0/0
625	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA ,	04/2016	5,200.00 -	1,700.43	48.00	03/2020 -	06/2023	39(O) -	0/0
626	QADIAN-BEAS - [N22000295]NR,PUNJAB ,	04/2011	205.22 -	205.22	1.89	- -	03/2024	- -	0/0
627	DAUSA-GANGAPUR CITY(NL) NWR - [220100184]NWR,RAJASTHAN ,	02/1997	410.08 780.98	886.41	525.78	02/2019 -	03/2021	25(O) -	0/0
628	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN ,	04/2012	246.08 -	348.55	215.47	12/2019 -	06/2020	6(O) -	0/0
629	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN ,	04/2013	236.93 -	294.90	141.40	10/2018 -	10/2019	12(O) -	0/0
630	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN ,	04/2013	822.00 -	1,099.54	.00	- -	-	-	0/1
631	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN ,	04/2013	323.00 -	432.22	.00	- -	-	-	0/0
632	MAVLI JUNCTION-BARI SADRI MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN ,	04/2013	420.18 -	420.18	160.53	03/2020 -	06/2020	3(O) -	0/0
633	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN ,	04/2011	213.39 -	303.56	262.32	11/2019 -	05/2020	6(O) -	0/0
634	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN ,	04/2013	242.09 281.03	410.00	351.23	02/2019 -	05/2020	15(O) -	0/0
635	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN ,	05/2015	873.71 -	1,980.21	4.25	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
636	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN ,	01/2011	493.17 -	493.17	439.80	03/2018 -	03/2020	24(O) -	0/0
637	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN ,	08/2018	808.85 -	808.85	47.07	08/2022 -	09/2022	1(O) -	0/0
638	SEVOK RANGPO NEFR - [N22000102]NFR,SIKKIM ,	04/2008	1,339.48 -	4,084.69	285.46	12/2015 -	-	-	0/0
639	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU ,	09/1995	303.98 -	980.00	669.21	03/2020 -	03/2021	12(O) -	0/0
640	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS MTP - [N22000028]MRTP,TAMIL NADU ,	04/2006	495.74 -	734.01	445.91	06/2013 -	-	-	1/4
641	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU ,	09/2007	724.69 -	2,072.50	1,386.59	02/2019 -	02/2020	12(O) -	0/0
642	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU ,	09/2006	227.40 -	900.00	62.50	-	-	-	0/0
643	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU ,	09/2006	582.83 -	2,300.00	241.39	-	-	-	0/0
644	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU ,	04/2008	151.84 -	1,105.00	3.34	02/2019 -	-	-	0/0
645	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU ,	04/2013	839.00 -	1,500.00	.62	-	-	-	0/0
646	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU ,	04/1999	198.68 -	556.64	303.72	-	-	-	0/0
647	ERODE-PALANI - [N22000199]SR,TAMIL NADU ,	04/2008	288.57 -	1,140.00	1.63	-	-	-	0/0
648	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU ,	04/2008	164.41 -	450.00	151.50	-	03/2020	-	0/0
649	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU ,	04/2007	931.98 -	951.24	724.96	-	03/2020	-	0/0
650	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU ,	10/2013	187.26 -	231.67	108.34	04/2014 -	03/2020	71(O) -	0/0
651	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU ,	02/1996	268.87 -	950.00	927.86	03/2005 -	-	-	0/0
652	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU ,	02/1999	257.00 257.00	257.00	268.31	03/2018 -	-	-	0/0
653	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU ,	02/2017	1,567.00 -	1,567.00	.00	03/2024 -	03/2026	24(O) -	0/0
654	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU ,	02/2015	1,700.00 -	1,003.00	167.73	03/2022 -	03/2022	0(O) -	0/0
655	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU ,	02/2015	760.00 -	1,182.31	406.32	03/2020 -	06/2021	15(O) -	0/0
656	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA ,	07/1998	458.25 -	458.26	3.83	-	-	-	0/0
657	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA ,	04/2006	1,160.48 -	1,160.48	288.38	03/2010 -	03/2023	156(O) -	1/1
658	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA ,	04/2012	632.68 -	816.55	686.11	03/2016 -	12/2020	57(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
659	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA ,	04/2013	1,112.00 -	2,911.84	.92	-	-	-	1/1
660	KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA ,	04/2013	723.00 -	997.09	.00	-	-	-	0/1
661	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES,TELANGANA ,	03/2015	636.38 -	636.38	281.85	03/2021 -	03/2021	0(O) -	3/3
662	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA ,	04/2015	773.94 -	773.94	413.71	12/2024 -	12/2024	0(O) -	0/0
663	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA ,	04/2017	119.73 185.00	184.97	3.67	03/2022 -	03/2022	0(O) -	0/0
664	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA ,	04/2012	569.63 -	650.00	45.24	03/2020 -	12/2021	21(O) -	2/3
665	ETAWAH-MAINPURI (NL) NCR - [220100318]NCR,UTTAR PRADESH ,	04/1997	120.00 -	346.00	345.51	12/2008 -	-	-	0/0
666	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH ,	02/2008	171.10 -	275.08	141.55	03/2012 -	-	-	0/0
667	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH ,	03/2013	307.00 -	1,409.09	.00	-	-	-	0/0
668	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH ,	03/2013	643.00 -	644.00	.00	-	-	-	0/0
669	UNCHAHAAR-AMETHI - [N22000294]NR,UTTAR PRADESH ,	04/2012	1,229.00 -	1,230.00	103.17	-	03/2023	-	0/0
670	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH ,	04/2014	182.92 -	197.73	.00	-	-	-	0/0
671	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH ,	03/2015	1,295.42 -	1,295.42	328.56	03/2022 -	12/2019	-27(O) -	0/0
672	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR,UTTAR PRADESH ,	04/2015	668.70 668.00	680.00	330.00	03/2020 -	03/2020	0(O) -	4/6
673	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH ,	04/2015	943.60 -	750.56	372.23	03/2022 -	12/2024	33(O) -	0/0
674	LUCKNOW- PILIBHIT VIA SITAPUR LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH ,	04/2011	927.01 -	1,200.00	1,147.34	03/2019 -	03/2020	12(O) -	0/0
675	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH ,	04/2015	1,765.92 -	1,765.92	601.87	03/2023 -	12/2024	21(O) -	0/0
676	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH ,	03/2012	1,183.25 -	1,183.25	1,072.44	12/2020 -	12/2022	24(O) -	0/0
677	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH ,	08/2015	2,436.21 -	2,436.21	517.46	03/2020 -	03/2021	12(O) -	0/0
678	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH ,	08/2015	528.57 -	528.57	107.81	03/2019 -	12/2019	9(O) -	0/0
679	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH ,	04/2016	213.00 -	213.35	8.97	04/2016 -	06/2020	50(O) -	0/0
680	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH ,	04/2016	1,900.00 -	1,277.06	.00	01/2022 -	01/2022	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
681	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH ,	04/2017	150.00 -	150.00	.00	04/2017 -	10/2022	66(O) -	0/0
682	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH ,	04/2017	1,343.00 -	1,476.15	.00	01/2018 -	-	-	0/0
683	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH ,	04/2017	622.50 427.00	426.74	179.51	04/2017 -	01/2020	33(O) -	0/0
684	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH ,	04/2017	276.90 -	276.90	.00	04/2017 -	04/2022	60(O) -	0/0
685	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH ,	04/2016	602.50 -	714.34	17.35	-	-	-	0/0
686	AUNRIHAR - JAUNPUR PATCH DOUBLING. - [N22000469]NER,UTTAR PRADESH ,	04/2016	600.00 -	600.00	25.24	01/2022 -	01/2022	0(O) -	0/0
687	SHAHGANJ-BHATNI-PHEPHNA-INDARA MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH ,	04/2016	1,177.96 -	1,028.95	26.06	12/2019 -	04/2021	16(O) -	0/0
688	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH ,	03/2018	4,329.53 -	4,329.53	3.90	03/2023 -	03/2023	0(O) -	0/0
689	JHANSI BINA DOUBLING - [N22000496]NCR,UTTAR PRADESH ,	09/2016	2,001.00 -	2,001.00	416.59	03/2021 -	03/2021	0(O) -	0/6
690	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND ,	04/2003	142.45 -	228.40	.15	-	-	-	0/0
691	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND ,	04/2012	219.83 -	346.63	229.48	-	06/2020	-	0/0
692	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND ,	04/2011	16,216.00 -	16,216.00	1,655.10	12/2024 -	03/2025	3(O) -	0/0
693	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL) NEFR - [220100135]NFR,WEST BENGAL ,	04/1983	297.32 -	614.00	274.97	03/2019 -	03/2020	12(O) -	0/0
694	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL ,	04/1974	393.46 154.30	1,026.00	182.49	03/2007 03/2007	-	-	0/0
695	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL ,	03/2000	1,049.69 -	3,404.92	3,837.57	12/2006 -	-	-	0/0
696	TARAKESWAR - BISHNUPUR NEW BG LINE (NL) ER - [220100272]ER,WEST BENGAL ,	04/2000	1,188.91 -	1,619.48	868.58	03/2019 12/2009	03/2025	72(O) 0	0/0
697	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL ,	04/2007	1,106.62 -	1,091.59	839.63	12/2010 12/2017	03/2025	171(O) 0	7/7
698	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL,WEST BENGAL ,	04/2010	2,397.72 -	2,397.72	197.20	03/2016 -	-	-	0/0
699	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL ,	04/2010	2,298.42 -	2,733.86	40.13	03/2014 -	12/2025	141(O) -	0/0
700	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL ,	04/2010	3,951.98 -	4,259.48	2,237.39	03/2016 -	03/2025	108(O) -	0/0
701	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL ,	04/2010	2,913.51 -	2,913.50	849.88	03/2016 -	03/2025	108(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
702	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL ,	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	63(O) -	0/0
703	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL ,	04/2010	267.37 -	620.00	40.99	- 03/2025	03/2025	- 0	0/0
704	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL ,	04/2010	221.42 -	380.00	38.18	- 03/2022	03/2022	- 0	0/0
705	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL ,	04/2009	573.78 -	268.52	.03	- -	03/2025	- -	0/0
706	BAZAR SAU - AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL ,	04/2012	255.64 -	272.20	166.12	- -	09/2021	- -	0/0
707	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR, WEST BENGAL ,	04/2016	602.27 -	612.00	257.73	12/2021 -	03/2020	-21(O) -	0/0
708	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER, WEST BENGAL ,	04/1998	1,027.40 -	2,373.00	485.04	03/2003 03/2030	03/2030	324(O) 0	0/0
709	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]NFR, WEST BENGAL ,	02/1999	380.60 -	1,871.00	1,087.60	04/2010 -	-	-	0/0
	Total		4,61,117.38 -	6,64,220.06	1,91,222.36				27/137
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
710	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL, A & N ISLANDS ,	03/2015	262.97 -	262.97	.00	10/2018 -	-	-	0/4
711	2 LANE WITH HARD SHOULDER REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL, A & N ISLANDS ,	03/2017	409.85 -	409.85	21.11	12/2017 -	-	-	0/4
712	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL, A & N ISLANDS ,	03/2015	277.17 -	277.17	148.80	04/2017 -	-	-	3/4
713	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL, A & N ISLANDS ,	02/2018	391.00 -	391.00	22.17	10/2018 -	-	-	0/4
714	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL, A & N ISLANDS ,	03/2018	234.27 -	234.27	19.87	10/2018 -	-	-	0/4
715	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MORTH, A & N ISLANDS ,	11/2017	237.80 -	238.00	7.48	11/2019 -	11/2019	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
716	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MORTH,A & N ISLANDS ,	11/2017	257.34 -	238.00	41.09	11/2019 -	11/2019	0(O) -	0/0
717	AJANTHA TO BULDHANA - [N24001008]MORTH,A & N ISLANDS ,	02/2017	401.00 401.00	401.00	98.81	07/2019 -	07/2019	-	0/4
718	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH , PPP (BOT)	04/2011	571.00 -	571.00	582.53	10/2013 -	-	-	0/0
719	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2011	1,535.00 -	1,535.00	3,220.15	05/2014 -	10/2019	65(O) -	0/0
720	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH.0.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH ,	07/2015	333.21 333.21	333.21	256.11	12/2015 -	-	-	0/2
721	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH , EPC	01/2014	195.45 -	195.45	.00	11/2014 -	-	-	0/4
722	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH , EPC	03/2015	271.45 -	271.45	152.90	10/2015 11/2019	11/2019	49(O) 25	3/4
723	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH.0.0) - [N24000302]PWD,ANDHRA PRADESH ,	07/2015	333.21 -	333.21	256.11	12/2015 -	-	-	0/2
724	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH , EPC	10/2015	333.21 -	353.89	256.11	11/2015 -	-	-	0/0
725	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH ,	01/2016	1,134.97 -	1,134.97	21.73	11/2018 -	-	-	0/0
726	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH ,	09/2014	1,684.00 -	1,684.00	54.13	02/2017 -	-	-	0/0
727	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]NHAI,ANDHRA PRADESH ,	03/2017	648.32 -	503.10	497.15	03/2020 -	11/2019	-4(O) -	0/0
728	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH ,	03/2017	1,041.62 -	1,187.10	778.87	03/2020 -	05/2020	2(O) -	0/0
729	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH , Central Sector Projects	06/2017	648.33 -	306.00	151.65	06/2017 -	11/2019	29(O) -	0/0
730	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH ,	12/2017	328.67 -	328.67	176.29	- -	11/2019	- -	0/0
731	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH ,	12/2017	1,323.15 -	1,323.15	345.33	- -	07/2021	- -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
732	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE OF - [N24000720]NHAI,ANDHRA PRADESH ,	12/2017	357.00 -	357.00	70.71	- -	-	-	0/0
733	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH ,	02/2018	1,959.00 -	1,959.00	597.16	- -	07/2021	- -	0/0
734	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH ,	03/2018	1,532.62 2,499.00	2,499.00	569.15	03/2021 -	04/2021	1(O) -	1/4
735	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH ,	03/2018	1,550.98 -	1,550.98	569.27	- -	07/2021	- -	0/0
736	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH ,	03/2018	565.09 -	565.09	120.20	- -	02/2021	- -	0/0
737	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH ,	03/2018	314.43 -	314.43	24.90	- -	12/2020	- -	0/0
738	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH ,	03/2018	557.30 -	557.30	177.12	- -	03/2020	- -	0/0
739	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]MORTH,ANDHRA PRADESH ,	10/2015	333.21 -	355.89	265.48	12/2015 12/2019	12/2019	48(O) 36	2/3
740	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929]MORTH,ANDHRA PRADESH ,	09/2016	372.68 -	372.68	183.25	02/2017 12/2019	12/2019	34(O) 10	2/4
741	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO - [N24000930]MORTH,ANDHRA PRADESH ,	11/2016	378.24 -	378.24	248.70	01/2018 01/2020	01/2020	24(O) 0	3/4
742	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931]MORTH,ANDHRA PRADESH ,	11/2016	290.15 -	290.15	69.47	05/2017 03/2020	03/2020	34(O) 10	1/4
743	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932]MORTH,ANDHRA PRADESH ,	01/2017	319.28 -	319.28	103.79	08/2017 03/2020	03/2020	31(O) 7	1/4
744	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]MORTH,ANDHRA PRADESH ,	02/2017	429.43 -	429.43	203.52	11/2017 03/2020	11/2019	24(O) 0	3/4

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
745	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934]MORTH,ANDHRA PRADESH ,	03/2018	228.32 -	228.32	34.74	08/2018 03/2020	03/2020	19(O) 0	1/4
746	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU - [N24000936]MORTH,ANDHRA PRADESH ,	03/2018	244.95 245.00	244.95	116.71	08/2018 02/2020	02/2020	18(O) 0	0/3
747	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]MORTH,ANDHRA PRADESH ,	03/2018	289.67 290.00	289.67	80.77	08/2018 02/2020	02/2020	18(O) 0	2/4
748	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938]MORTH,ANDHRA PRADESH ,	03/2018	297.12 294.00	294.12	189.72	07/2018 01/2020	01/2020	18(O) 0	4/4
749	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]MORTH,ANDHRA PRADESH ,	03/2018	504.19 504.00	504.19	201.11	11/2018 05/2020	05/2020	18(O) 0	2/4
750	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]MORTH,ANDHRA PRADESH ,	03/2016	995.09 995.00	995.09	401.90	05/2016 03/2020	03/2020	46(O) 22	2/4
751	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963]MORTH,ANDHRA PRADESH ,	01/2018	418.03 -	418.03	144.09	08/2018 08/2020	08/2020	24(O) 0	2/4
752	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964]MORTH,ANDHRA PRADESH ,	08/2016	350.61 -	350.61	303.82	01/2017 12/2019	12/2019	35(O) 17	3/4
753	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]MORTH,ANDHRA PRADESH ,	01/2016	386.09 -	386.09	182.98	05/2016 08/2019	05/2018	-	2/4
754	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966]MORTH,ANDHRA PRADESH ,	01/2016	348.95 -	348.95	161.18	08/2016 03/2020	03/2020	43(O) 19	2/4
755	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967]MORTH,ANDHRA PRADESH ,	03/2016	444.84 -	444.84	234.31	09/2016 03/2020	03/2020	42(O) 18	2/4
756	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]MORTH,ANDHRA PRADESH ,	11/2016	376.25 -	376.25	196.09	08/2017 03/2020	03/2020	31(O) 7	2/4
757	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969]MORTH,ANDHRA PRADESH ,	01/2017	263.45 -	263.45	57.97	09/2017 03/2020	09/2019	24(O) 0	0/4
758	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]MORTH,ANDHRA PRADESH ,	01/2017	576.48 -	576.48	207.93	01/2018 03/2020	01/2020	24(O) 0	1/4

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
759	REHABILITATION & UPGRADE OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S - [N24001183]PWD, ANDHRA PRADESH ,	07/2014	251.55 -	251.55	7.74	02/2015 -	-	-	0/0
760	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD, ARUNACHAL PRADESH , ITEM RATE	12/2011	156.63 276.00	276.00	147.65	02/2012 -	-	-	0/0
761	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD, ARUNACHAL PRADESH , ITEM RATE	11/2010	305.49 -	305.49	131.08	03/2011 -	-	-	0/0
762	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM 75.00) IN ARUNACHAL PR - [N24000311]PWD, ARUNACHAL PRADESH , ITEM RATE	03/2012	207.03 389.45	389.45	275.19	05/2012 06/2018	-	-	0/0
763	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL, ARUNACHAL PRADESH , EPC	03/2015	194.11 -	194.11	178.14	05/2018 -	08/2019	-	3/4
764	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL, ARUNACHAL PRADESH , EPC	10/2015	179.82 -	179.82	197.77	01/2019 -	-	-	4/4
765	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL, ARUNACHAL PRADESH , EPC	07/2015	197.16 197.16	197.16	66.17	10/2018 09/2015	09/2018	-	1/4
766	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL, ARUNACHAL PRADESH , EPC	03/2015	394.00 -	394.00	272.92	06/2018 -	03/2020	21(O) -	1/3
767	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450 TO KM 605.600 (EXISTING CHAINAGE FROM KM 583.450 - [N24000614]NHIDCL, ARUNACHAL PRADESH ,	01/2016	183.65 -	183.65	98.02	11/2016 -	-	-	2/4
768	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL, ARUNACHAL PRADESH ,	04/2016	245.79 -	245.79	98.37	- -	09/2020	- -	2/4
769	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL, ARUNACHAL PRADESH ,	04/2016	198.00 -	198.00	155.94	10/2016 -	10/2019	36(O) -	3/4
770	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL, ARUNACHAL PRADESH ,	11/2015	434.06 -	434.06	131.32	- -	12/2020	- -	2/4
771	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL, ARUNACHAL PRADESH ,	12/2016	138.93 155.00	155.00	72.97	01/2017 -	01/2020	36(O) -	2/4

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
772	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH ,	01/2017	1,253.10 -	1,253.10	158.90	03/2017 -	03/2022	60(O) -	1/4
773	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH ,	03/2017	284.09 284.09	284.09	76.20	04/2017 03/2018	03/2021	47(O) 0	1/4
774	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH ,	02/2017	195.23 -	195.23	37.30	04/2017 -	-	-	1/4
775	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH ,	02/2017	203.36 -	203.36	49.12	04/2017 -	-	-	1/4
776	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH ,	01/2017	194.66 -	194.66	75.04	04/2017 -	-	-	1/4
777	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH ,	02/2017	168.32 168.32	168.32	33.51	04/2017 02/2018	02/2021	46(O) 0	1/4
778	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH ,	02/2017	180.57 180.57	180.57	13.73	04/2017 02/2018	02/2021	46(O) 0	0/4
779	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH ,	02/2017	216.71 216.71	216.71	16.40	04/2017 02/2018	02/2021	46(O) 0	0/4
780	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH ,	02/2017	167.28 167.28	167.28	18.94	04/2017 02/2018	02/2021	46(O) 0	1/1
781	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH ,	01/2017	198.22 -	198.22	24.14	04/2017 -	-	-	1/4
782	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH ,	03/2018	392.60 -	392.60	.00	- -	-	-	0/0
783	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH ,	12/2016	200.44 -	200.44	20.03	- -	-	-	0/0
784	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH ,	03/2017	1,718.59 -	1,718.59	158.90	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
785	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 37.500 TO KM - [N24000947]NHIDCL,ARUNACHAL PRADESH ,	05/2016	259.52 -	259.52	155.94	- -	-	-	0/0
786	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH ,	09/2016	568.92 -	568.92	131.32	- -	-	-	0/0
787	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH ,	12/2016	188.78 -	188.78	38.37	- -	-	-	0/0
788	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH ,	02/2017	175.06 175.06	175.06	12.06	- 04/2019	04/2022	- 0	0/0
789	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL,ARUNACHAL PRADESH ,	02/2017	176.12 176.12	176.12	11.82	- 04/2019	04/2022	- 0	0/0
790	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D - [N24000974]NHIDCL,ARUNACHAL PRADESH ,	02/2017	199.02 199.02	199.02	9.81	- 02/2018	02/2021	- 0	0/0
791	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D - [N24000975]NHIDCL,ARUNACHAL PRADESH ,	02/2017	184.88 184.88	184.88	6.19	- 02/2018	02/2021	- 0	0/0
792	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL,ARUNACHAL PRADESH ,	10/2015	210.50 210.50	210.50	117.06	- 01/2016	01/2019	-	0/0
793	BORDUMSA NAMCHIK (BURIDEHING - JAIRAMPUR) ROAD ON NH-52B (NEW NH-215) FROM KM. 0.15 (STARTING CHAIN - [N24000977]NHIDCL,ARUNACHAL PRADESH ,	07/2015	189.91 -	189.91	154.43	- -	-	-	4/4
794	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN - [N24000978]NHIDCL,ARUNACHAL PRADESH ,	03/2015	172.75 -	172.75	112.43	- -	-	-	3/4
795	TWO-LANING OF HAYULIANG– HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI - [N24000979]NHIDCL,ARUNACHAL PRADESH ,	01/2017	256.66 -	256.66	24.14	- -	-	-	1/4
796	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MORTH,ARUNACHAL PRADESH ,	09/2011	1,979.00 -	1,979.00	59.40	- -	-	-	0/0
797	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]PWD,ARUNACHAL PRADESH ,	11/2016	243.89 -	243.89	30.04	- -	-	-	0/0
798	HARANGAJO TO MAIBANG (AS-23) KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM ,	12/2003	280.00 456.92	525.00	488.37	02/2009 07/2019	07/2019	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
799	MAIBANG TO LUMDING (AS-25) KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM ,	12/2003	199.81 340.14	340.14	319.96	04/2009 03/2011	08/2019	-	0/0
800	MAIBANG TO LUMDING (AS-26) KM.60.500 TO KM.83.400 NH-54 - [240106279]NHAI,ASSAM ,	12/2003	167.64 408.77	408.77	395.78	11/2008 07/2011	01/2014	-	0/0
801	MAIBANG TO LUMDING (AS-24) KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM ,	12/2003	155.04 255.23	255.23	251.39	11/2008 01/2011	08/2013	-	0/0
802	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM ,	12/2003	245.00 -	174.34	224.28	03/2008 -	08/2020	149(O) -	0/0
803	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM ,	12/2003	225.00 -	225.00	328.47	06/2008 -	10/2019	136(O) -	0/0
804	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM ,	12/2003	208.00 -	230.00	337.76	04/2008 -	03/2020	143(O) -	0/0
805	DHARAMTUL TO SONAPUR KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM ,	12/2003	160.00 -	167.98	223.81	05/2008 -	06/2019	-	0/0
806	HARANGAJO TO MAIBANG NH-54 - [N24000062]NHAI,ASSAM ,	12/2003	196.00 655.17	655.17	655.17	07/2009 10/2018	10/2018	-	0/0
807	BRAHMPUTRA BRIDGE NH NO-31 - [N24000063]NHAI,ASSAM ,	12/2003	217.61 -	360.84	451.15	04/2010 -	07/2019	-	0/0
808	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N240000305]NHIDCL,ASSAM , EPC	05/2015	454.89 -	454.89	123.20	05/2018 05/2020	12/2020	31(O) 0	2/4
809	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N240000319]NHIDCL,ASSAM , EPC	06/2015	437.39 -	437.39	9.30	06/2018 12/2020	12/2021	42(O) 0	0/4
810	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N240000320]NHIDCL,ASSAM , EPC	06/2015	463.49 -	463.49	22.32	06/2018 01/2021	12/2021	42(O) 0	0/4
811	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N240000321]NHIDCL,ASSAM , EPC	06/2016	829.00 -	829.00	343.57	01/2019 -	-	-	2/4
812	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N240000322]NHIDCL,ASSAM , EPC	03/2015	168.39 -	168.39	78.89	11/2018 -	-	-	4/4
813	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N240000323]NHIDCL,ASSAM , EPC	10/2014	588.95 -	588.95	366.26	11/2018 -	-	-	2/4
814	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N240000392]PWD,ASSAM , EPC	11/2010	268.08 -	268.08	201.56	05/2017 -	-	-	0/0
815	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N240000396]PWD,ASSAM , ITEM RATE	11/2010	470.20 -	630.36	344.32	02/2011 -	-	-	0/0
816	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N240000411]PWD,ASSAM , EPC	11/2014	218.31 307.47	307.47	256.26	02/2018 -	-	-	0/0
817	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N240000429]NHIDCL,ASSAM , EPC	12/2015	225.02 -	159.20	26.00	12/2018 -	-	-	1/4
818	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N240000430]NHIDCL,ASSAM , EPC	12/2015	223.30 -	223.30	78.89	06/2018 -	-	-	1/4

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
819	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM , EPC	01/1991	520.01 -	520.01	57.36	- -	-	-	1/4
820	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM , EPC	12/2015	289.99 -	289.99	20.97	12/2018 -	-	-	0/4
821	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM , EPC	01/2016	294.17 -	294.17	63.00	01/2016 02/2019	04/2021	63(O) 0	1/4
822	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM , EPC	01/2016	252.00 -	252.00	4.74	01/2016 12/2021	12/2021	71(O) 0	0/4
823	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM ,	03/2015	829.00 -	829.00	343.57	01/2016 -	-	-	2/3
824	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL,ASSAM ,	10/2017	818.00 -	818.00	60.08	- -	06/2020	- -	0/4
825	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0 KM 54/0 TO KM 61/0 KM 69/0 TO KM 80/0 AN - [N24001152]PWD,ASSAM ,	09/2018	160.00 -	160.00	.50	09/2021 -	09/2021	0(O) -	0/0
826	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM - [N24001153]PWD,ASSAM ,	11/2010	197.37 -	197.37	88.86	02/2014 -	12/2019	70(O) -	0/0
827	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL,ASSAM ,	03/2017	1,049.51 -	1,049.51	86.70	- -	-	-	0/0
828	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR , PPP (ANNUITY)	08/2010	671.30 -	671.30	885.47	02/2013 -	-	-	0/0
829	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR , PPP (ANNUITY)	05/2011	351.54 -	351.54	329.40	05/2013 -	-	-	0/0
830	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR , PPP (BOT)	09/2011	574.00 -	574.00	768.73	03/2014 -	-	-	0/0
831	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR ,	10/2011	375.09 -	375.09	494.33	04/2014 -	-	-	0/0
832	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR , PPP (ANNUITY)	01/2011	575.00 -	575.00	843.67	07/2013 -	-	-	0/0
833	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR , PPP (ANNUITY)	05/2011	511.54 -	511.54	566.60	11/2013 -	-	-	0/0
834	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR , EPC	01/1991	675.00 -	780.77	152.37	- -	-	-	0/0
835	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR , ITEM RATE	01/1991	282.41 -	322.01	278.45	08/2016 -	-	-	0/0
836	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR , ITEM RATE	01/1991	358.22 -	377.64	323.60	10/2016 -	-	-	0/0
837	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR ,	08/2015	556.07 -	556.07	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
838	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR ,	12/2015	1,041.10 -	1,041.10	214.34	04/2019 -	-	-	0/0
839	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR ,	08/2015	814.04 -	814.04	384.48	-	01/2020	-	0/0
840	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR ,	08/2015	322.09 -	322.09	77.53	04/2018 -	04/2020	24(O) -	0/0
841	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR ,	01/1991	642.41 -	642.41	131.71	-	10/2020	-	0/0
842	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR ,	12/2015	1,167.45 -	1,167.45	113.26	-	12/2019	-	0/0
843	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR ,	08/2015	399.54 -	399.54	195.59	04/2019 -	10/2019	6(O) -	0/0
844	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR ,	01/1991	478.35 -	478.35	.00	-	-	-	0/0
845	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR ,	08/2015	854.80 -	854.80	579.78	-	-	-	0/0
846	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR ,	08/2015	516.13 -	516.13	417.09	04/2018 -	-	-	0/0
847	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR , EPC	01/1991	154.62 -	154.62	.00	-	-	-	0/0
848	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR , EPC	01/1991	319.68 -	369.77	113.67	-	-	-	0/0
849	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR ,	10/2013	278.39 -	278.39	.00	08/2014 -	-	-	0/0
850	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR ,	11/2013	683.83 -	683.83	596.44	07/2016 -	-	-	0/0
851	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR ,	02/2014	665.50 -	665.50	.00	07/2016 -	-	-	0/0
852	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR ,	02/2016	178.85 -	178.85	93.11	05/2016 -	-	-	0/0
853	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR ,	02/2016	369.77 -	369.77	.00	06/2016 -	-	-	0/0
854	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR ,	02/2016	553.30 -	553.30	267.22	05/2016 -	-	-	0/0
855	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR ,	01/2014	1,408.85 -	1,408.85	753.03	10/2016 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
856	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPR - [N24000580]MORTH,BIHAR ,	03/2015	206.80 -	206.80	74.04	07/2016 -	-	-	0/0
857	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR ,	08/2015	288.24 -	288.24	280.00	11/2015 -	-	-	0/0
858	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI,BIHAR ,	05/2015	581.84 -	581.84	77.43	05/2017 -	-	-	0/0
859	REHABILITATION OF 4-LANE 5.575 KM LONG 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR ,	08/2016	1,742.01 -	1,742.01	719.20	12/2016 -	-	-	0/0
860	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR ,	03/2017	672.89 -	736.01	.00	03/2020 -	03/2020	0(O) -	0/0
861	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR ,	03/2017	235.48 -	227.77	.00	03/2020 -	05/2021	14(O) -	0/0
862	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR , Central Sector Projects	08/2017	950.64 -	950.64	102.51	08/2017 -	02/2022	54(O) -	0/0
863	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR ,	12/2017	2,598.00 -	2,598.00	.00	- -	-	-	0/0
864	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR ,	01/2018	573.70 -	573.70	.00	- -	-	-	0/0
865	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR ,	01/2018	895.39 -	895.39	.00	- -	-	-	0/0
866	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR ,	03/2018	496.20 -	496.20	.00	- -	-	-	0/0
867	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MORTH,BIHAR ,	09/2018	1,478.40 -	1,478.40	.00	- -	-	-	0/0
868	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C - [N24000999]PWD,BIHAR ,	11/2016	230.34 -	230.34	178.39	10/2019 -	10/2019	0(O) -	0/0
869	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]PWD,BIHAR ,	03/2018	153.24 -	153.24	2.06	- -	-	-	0/0
870	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]PWD,BIHAR ,	05/2014	199.98 -	199.98	153.43	08/2016 -	12/2020	52(O) -	0/0
871	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]PWD,BIHAR ,	02/2019	2,926.42 -	2,926.42	.00	- -	-	-	0/0
872	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH , EPC	12/2015	291.05 -	291.05	181.90	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
873	REHABILITATION AND UPGRADEMENT OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH , EPC	11/2015	485.44 -	485.44	445.75	12/2015 -	-	-	0/0
874	FOUR LANE OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH ,	12/2015	596.67 -	596.67	392.06	05/2018 10/2019	10/2019	17(O) 0	0/0
875	FOUR LANE OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH ,	12/2015	509.13 -	509.13	412.66	04/2018 08/2018	08/2018	-	0/0
876	FOUR / SIX LANE OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH ,	12/2015	726.67 598.13	598.13	414.73	04/2018 03/2020	03/2020	23(O) 0	0/0
877	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH ,	03/2018	1,029.96 -	1,261.05	97.55	- 03/2021	03/2021	- 0	0/0
878	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]NHAI,DELHI ,	09/2015	771.18 -	7,558.00	261.77	- -	-	-	0/0
879	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8 - [N24001184]NHIDCL,DELHI ,	07/2017	269.69 -	269.69	.00	09/2019 -	12/2019	3(O) -	0/0
880	FOUR LANE OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDEAPAR BRIDGE - [N24000251]NHDP,GOA , EPC	03/2015	297.00 -	297.00	290.64	04/2018 -	-	-	0/1
881	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA ,	03/2015	298.33 -	298.33	153.33	- -	-	-	0/4
882	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]DORTH,GOA , EPC	03/2015	184.05 -	184.05	91.39	- -	-	-	2/4
883	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA , EPC	03/2015	280.16 -	290.59	280.47	- -	-	-	3/4
884	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA , EPC	10/2015	936.40 -	936.40	262.25	- -	-	-	0/0
885	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA , EPC	12/2015	773.98 -	773.98	259.46	- -	-	-	0/0
886	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUARI - [N24000516]MORTH,GOA , EPC	12/2015	819.95 -	819.95	191.63	- -	-	-	0/0
887	PATRADEVI TO KARASWADA 4L - [N24001004]MORTH,GOA ,	03/2017	634.32 634.32	634.32	102.33	05/2020 -	05/2020	0(O) -	1/4
888	KARASWADA TO BAMBOLIM - [N24001005]MORTH,GOA ,	03/2017	852.67 852.67	852.67	108.04	12/2019 -	12/2019	0(O) -	1/4
889	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT , PPP (BOT)	03/2010	1,509.10 3,787.21	1,509.10	3,669.10	09/2012 12/2019	-	-	2/3
890	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT , PPP (BOT)	01/2011	953.88 -	953.88	976.79	07/2013 -	-	-	0/0
891	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT , PPP (BOT)	01/2013	2,125.24 2,521.24	2,521.24	4,659.71	12/2015 -	-	-	3/3

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
892	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT ,	03/2014	503.16 -	503.16	389.50	08/2016 -	-	-	0/0
893	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT ,	05/2016	998.18 -	998.18	435.25	- -	-	-	0/0
894	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT ,	05/2016	834.64 -	834.64	140.44	- -	10/2019	-	0/0
895	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT ,	05/2016	723.64 -	723.64	321.67	- -	09/2019	-	0/0
896	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT ,	05/2016	763.08 -	763.08	357.12	- -	-	-	0/0
897	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT ,	05/2016	425.60 241.41	425.60	97.78	- -	-	-	0/0
898	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT ,	05/2016	364.56 -	392.00	240.57	- -	12/2019	-	0/0
899	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT ,	07/2016	829.97 -	829.97	75.08	- -	01/2020	-	0/0
900	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT ,	12/2016	417.19 -	417.19	262.83	- -	09/2019	-	0/0
901	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT ,	01/2017	1,251.11 -	1,251.11	1,084.26	- -	01/2021	-	0/0
902	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT ,	06/2017	1,958.88 -	1,958.88	1,116.85	06/2020 -	08/2020	2(O) -	0/0
903	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT , Central Sector Projects	10/2017	232.49 -	232.49	.00	10/2017 -	11/2019	25(O) -	0/0
904	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT ,	02/2018	1,052.21 1,449.00	1,449.00	1,296.87	- -	01/2021	-	0/0
905	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT ,	03/2018	2,702.05 -	2,702.05	.00	- -	01/2021	-	0/0
906	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT ,	03/2018	1,437.64 1,687.00	1,437.64	457.31	- 12/2018	07/2021	- 0	0/0
907	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT ,	03/2018	1,161.39 1,404.00	1,161.39	.00	- 11/2021	-	-	0/0
908	WIDENING FROM TWO LANE TO FOUR LANE WITH PAVED SHOULDER AND STRENGTHNING OF EXISTING PAVEMENT BETWEE - [N24000920]PWD,GUJARAT ,	03/2016	223.67 -	223.67	112.81	02/2017 -	-	-	4/4
909	UPGRADATION TO 2 LANE WITH PAVED SHOULDER WITH RIGID PAVEMENTS FROM 37/400 TO KM 66/700 ON NH 848 ON - [N24000921]PWD,GUJARAT , EPC	03/2016	208.34 -	208.34	112.87	02/2016 -	-	-	0/4

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
910	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922]PWD, GUJARAT , EPC	12/2017	867.97 -	867.97	90.63	11/2018 -	-	-	0/1
911	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEEN - [N24000923]PWD, GUJARAT , EPC	03/2018	464.07 -	464.07	14.17	11/2018 -	-	-	0/1
912	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]PWD, GUJARAT , EPC	10/2018	400.76 -	400.76	4.45	05/2019 -	-	-	0/0
913	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926]PWD, GUJARAT , EPC	08/2017	962.43 -	962.43	45.70	03/2018 -	-	-	0/1
914	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197]PWD, GUJARAT ,	03/2018	351.00 -	351.00	.48	06/2021 -	06/2021	0(O) -	0/0
915	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, HARYANA , PPP (BOT)	04/2007	486.00 -	486.00	470.01	05/2010 -	03/2020	118(O) -	0/0
916	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA , PPP (BOT)	05/2009	1,108.00 2,967.50	2,967.50	3,986.72	11/2011 -	03/2020	100(O) -	0/0
917	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI, HARYANA ,	08/2015	723.54 -	723.54	530.94	02/2018 -	-	-	0/0
918	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI, HARYANA ,	12/2015	602.95 507.70	507.70	495.63	06/2016 -	09/2019	39(O) -	0/0
919	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI, HARYANA ,	01/2016	574.28 537.16	537.16	500.61	07/2018 -	10/2019	15(O) -	0/0
920	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI, HARYANA , PPP (BOT)	07/2015	2,128.72 -	2,128.72	971.24	04/2019 -	-	-	0/0
921	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI, HARYANA ,	11/2015	867.66 -	867.66	502.66	05/2018 -	-	-	0/0
922	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI, HARYANA ,	08/2016	248.97 -	248.97	240.44	05/2019 -	12/2019	7(O) -	0/0
923	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI, HARYANA ,	09/2016	1,004.67 -	813.45	576.86	05/2019 -	02/2019	-	0/0
924	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI, HARYANA ,	03/2017	639.79 -	552.90	491.93	03/2020 -	09/2019	-6(O) -	0/0
925	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI, HARYANA ,	03/2018	1,484.30 -	1,484.30	45.34	-	12/2020	-	0/0
926	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI, HARYANA ,	03/2018	275.12 -	275.12	119.66	-	03/2020	-	0/0
927	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTI - [N24000837]NHAI, HARYANA ,	03/2018	307.79 -	307.79	140.10	-	03/2020	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
928	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA ,	03/2018	634.70 931.21	931.21	2.55	- -	07/2021	- -	0/0
929	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA ,	03/2018	795.50 -	799.30	80.90	- -	07/2021	- -	0/0
930	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA ,	03/2018	198.05 -	198.05	87.04	- -	03/2020	- -	0/0
931	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA ,	03/2018	181.78 -	181.78	52.50	- -	06/2020	- -	0/0
932	REDESIGNING REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA ,	03/2018	551.58 -	551.58	243.38	- -	03/2020	- -	0/0
933	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]PWD,HARYANA ,	01/2017	247.25 -	247.25	144.71	03/2019 03/2020	09/2019	6(O) 0	0/0
934	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) - [N24000908]PWD,HARYANA ,	01/2017	276.01 -	276.01	187.39	03/2019 07/2019	-	-	0/0
935	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI,HARYANA ,	01/2019	1,051.91 -	1,051.91	213.77	- -	-	-	0/0
936	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI,HARYANA ,	01/2019	1,120.06 -	1,120.06	228.51	- -	-	-	0/0
937	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA ,	01/2019	1,137.42 -	1,137.42	305.25	- -	-	-	0/0
938	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA ,	01/2019	1,033.19 -	1,033.19	209.38	- -	-	-	0/0
939	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA ,	01/2019	1,243.45 -	1,243.45	338.76	- -	-	-	0/0
940	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA ,	01/2019	889.36 -	889.36	251.12	- -	-	-	0/0
941	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA ,	01/2019	1,018.79 -	1,018.79	226.52	- -	-	-	0/0
942	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA ,	01/2019	996.65 -	996.65	286.25	- -	-	-	0/0
943	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH , PPP (BOT)	11/2013	1,916.79 -	1,916.79	1,948.92	11/2016 -	-	-	0/0
944	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH ,	09/2015	934.46 1,302.98	934.46	531.34	03/2018 -	03/2020	24(O) -	0/0
945	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH ,	02/2016	273.20 -	273.20	267.38	02/2019 -	06/2019	-	0/0
946	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH ,	08/2016	1,583.18 2,170.44	1,583.18	234.67	- -	09/2020	- -	0/0
947	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH ,	09/2016	1,273.71 -	1,273.71	.00	- -	07/2020	- -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
948	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH ,	10/2016	447.75 -	447.75	179.17	- -	11/2019	- -	0/0
949	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH ,	06/2017	2,485.93 -	2,485.93	704.29	06/2020 -	09/2021	15(O) -	0/0
950	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050 ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH ,	03/2018	478.74 1,071.75	478.74	15.06	- -	05/2021	- -	0/0
951	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,987.00 -	1,987.00	2,700.65	07/2015 12/2019	09/2020	62(O) 0	0/0
952	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	05/2011	2,159.00 2,519.00	2,519.00	4,705.68	06/2015 -	-	-	0/0
953	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,813.76 -	1,813.76	2,393.99	07/2013 -	-	-	0/0
954	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	06/2011	1,100.70 -	1,100.70	2,880.38	06/2014 09/2017	09/2020	75(O) 0	0/0
955	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR ,	12/2015	2,168.66 -	2,168.66	621.26	06/2019 -	12/2020	18(O) -	0/0
956	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR ,	12/2015	2,136.97 2,273.00	2,136.97	1,214.48	12/2018 12/2019	07/2020	19(O) 9	0/0
957	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR ,	12/2017	1,471.75 1,339.00	1,339.00	376.15	- -	01/2021	- -	1/3
958	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866]NHIDCL,JAMMU AND KASHMIR ,	03/2018	404.17 -	404.17	90.94	08/2018 -	-	-	1/4
959	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM - [N24000867]NHIDCL,JAMMU AND KASHMIR ,	03/2018	216.00 -	216.00	33.11	11/2018 -	-	-	0/4
960	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR ,	03/2018	253.44 -	253.44	.00	07/2019 -	-	-	0/0
961	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND , PPP (ANNUITY)	12/2012	1,479.00 -	1,479.00	740.26	06/2015 -	-	-	0/0
962	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND ,	02/2016	997.15 -	997.15	728.62	03/2019 -	07/2019	-	0/0
963	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND ,	07/2016	458.03 -	458.03	303.12	- 12/2017	12/2019	- 0	0/0
964	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND ,	08/2016	323.72 -	323.72	252.99	08/2018 -	01/2020	17(O) -	0/0
965	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]NHAI,JHARKHAND ,	03/2017	165.50 -	172.16	117.09	03/2020 -	09/2019	-6(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
966	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI,JHARKHAND ,	03/2017	239.68 -	235.90	91.24	03/2020 -	03/2020	0(O) -	0/0
967	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND ,	01/2018	273.46 -	273.46	.00	- -	-	-	0/0
968	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND ,	01/2018	1,155.16 -	1,155.16	.00	- -	-	-	0/0
969	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND ,	03/2018	1,005.08 1,073.10	1,005.08	.00	- 03/2019	03/2021	- 0	0/0
970	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSI PUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131]PWD,JHARKHAND ,	03/2018	212.99 -	212.99	80.47	06/2020 -	06/2020	0(O) -	0/0
971	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA ,	09/2010	946.00 -	946.00	818.53	06/2018 -	12/2019	18(O) -	3/3
972	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA , EPC	03/2015	165.67 -	165.67	.00	11/2015 -	-	-	0/0
973	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA , EPC	03/2015	159.12 -	159.12	.00	11/2015 -	-	-	0/0
974	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA , EPC	01/1991	219.40 -	219.40	.00	01/2018 -	-	-	0/0
975	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA , PPP (BOT)	05/2014	1,655.01 -	1,655.01	1,867.51	08/2016 -	12/2020	52(O) -	0/0
976	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA , PPP (BOT)	03/2015	1,388.00 -	1,388.00	1,153.07	08/2018 -	03/2020	19(O) -	0/0
977	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA ,	03/2016	701.40 -	701.40	29.48	03/2019 -	11/2020	20(O) -	0/0
978	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA ,	03/2016	870.00 -	870.00	36.30	03/2019 -	11/2020	20(O) -	0/0
979	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA ,	08/2016	1,664.20 -	1,664.20	657.08	04/2020 -	04/2020	0(O) -	0/0
980	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA ,	08/2016	1,167.42 870.00	870.00	254.96	03/2019 03/2017	08/2020	17(O) 0	0/0
981	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA ,	09/2016	950.69 1,008.00	1,108.00	1,354.09	08/2019 -	12/2020	16(O) -	0/0
982	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA ,	03/2017	831.58 -	1,177.00	586.20	03/2020 -	07/2020	4(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
983	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA ,	03/2017	993.16 -	1,434.00	645.75	03/2020 -	06/2020	3(O) -	0/0
984	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA ,	02/2018	486.78 -	486.78	113.59	- -	-	-	0/0
985	SIX-LANING OF BANGALORE – NIDAGATTA SECTION KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA ,	02/2018	1,995.34 2,190.00	2,400.00	1,555.77	- 05/2019	11/2021	- 0	0/0
986	SIX LANING OF NIDAGATTA-MYSORE SECTION KM 74.20 TO KM 135.304 OF NH-275 IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA ,	02/2018	2,177.80 2,283.50	2,450.00	793.30	- 10/2019	-	-	0/0
987	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT - [N24001154]PWD,KARNATAKA ,	08/2016	367.44 -	367.44	61.95	01/2017 -	-	-	0/0
988	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT - [N24001155]PWD,KARNATAKA ,	08/2016	175.20 -	175.20	113.38	01/2017 -	-	-	0/0
989	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA - [N24001156]PWD,KARNATAKA ,	01/2017	166.67 -	166.67	117.05	09/2017 -	-	-	0/0
990	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]PWD,KARNATAKA ,	08/2016	175.50 -	175.50	86.54	02/2017 -	-	-	0/0
991	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]PWD,KARNATAKA ,	03/2018	159.97 -	159.97	.00	06/2019 -	-	-	0/0
992	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]PWD,KARNATAKA ,	01/2018	159.70 -	159.70	22.79	07/2018 -	-	-	0/0
993	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]PWD,KARNATAKA ,	09/2017	191.60 -	191.60	26.24	10/2018 -	-	-	0/0
994	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- [N24001161]PWD,KARNATAKA ,	12/2017	297.30 -	297.30	.00	01/2019 -	-	-	0/0
995	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]PWD,KARNATAKA ,	03/2018	325.86 -	325.86	62.54	10/2018 -	-	-	0/0
996	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]PWD,KARNATAKA ,	08/2016	329.01 -	329.01	135.50	02/2017 -	-	-	0/0
997	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]PWD,KARNATAKA ,	10/2016	396.96 -	396.96	113.98	03/2017 -	-	-	0/0
998	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]PWD,KARNATAKA ,	11/2016	314.90 -	314.90	104.40	03/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
999	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]PWD,KARNATAKA ,	03/2015	159.12 -	159.12	96.22	01/2016 -	-	-	0/0
1000	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776) - [N24001167]PWD,KARNATAKA ,	03/2015	165.67 -	165.67	87.63	01/2016 -	-	-	0/0
1001	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]PWD,KARNATAKA ,	05/2018	171.60 -	171.60	.86	05/2018 -	05/2020	24(O) -	0/0
1002	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM. - [N24001170]PWD,KARNATAKA ,	01/2014	471.16 -	471.16	128.32	08/2014 -	-	-	0/0
1003	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]PWD,KARNATAKA ,	01/2017	291.49 -	291.49	130.00	08/2017 -	-	-	0/0
1004	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION - [N24001173]PWD,KARNATAKA ,	02/2017	157.32 188.00	157.32	.00	05/2019 -	05/2021	24(O) -	0/0
1005	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA , PPP (BOT)	02/2010	617.00 -	617.00	943.17	08/2012 -	12/2019	88(O) -	0/0
1006	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA , EPC	01/2014	255.75 348.00	348.43	290.12	09/2017 -	12/2019	27(O) -	0/0
1007	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA ,	06/2015	845.24 -	941.00	824.26	- -	10/2019	- -	0/0
1008	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26,500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA ,	04/2016	804.97 -	804.97	438.27	06/2018 -	04/2020	22(O) -	0/0
1009	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA , Central Sector Projects	09/2017	1,124.11 -	1,232.76	278.60	09/2017 -	06/2020	33(O) -	0/0
1010	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA ,	02/2018	1,424.77 -	1,853.42	14.19	- -	-	-	0/0
1011	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH , PPP (BOT)	10/2010	1,175.00 -	1,175.00	1,342.77	04/2013 -	-	-	0/4
1012	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH , PPP (BOT)	11/2010	325.00 -	325.00	469.54	05/2013 -	-	-	0/3
1013	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH , BOT (TOLL)	01/2012	320.48 -	320.48	189.49	08/2015 -	-	-	0/0
1014	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH , EPC	06/2015	390.51 -	390.51	191.77	- -	03/2020	- -	0/0
1015	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH , EPC	11/2013	497.05 -	881.05	544.84	05/2017 -	05/2020	36(O) -	0/0
1016	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH , BOT (TOLL)	08/2015	257.80 -	257.00	12.38	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1017	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH , BOT (TOLL)	11/2011	954.43 -	954.43	235.61	09/2015 -	03/2020	54(O) -	0/0
1018	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH , BOT (TOLL)	01/2012	410.72 -	410.72	216.14	04/2015 -	10/2019	54(O) -	0/0
1019	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH ,	03/2015	795.76 622.00	622.00	629.18	- -	10/2019	- -	0/0
1020	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH ,	03/2015	794.30 622.00	622.00	582.73	- -	10/2019	- -	0/0
1021	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH , EPC	11/2015	628.45 -	628.45	252.21	01/2020 -	01/2020	0(O) -	0/0
1022	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH , EPC	12/2015	957.54 -	957.54	467.50	02/2020 -	02/2020	0(O) -	0/0
1023	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH ,	03/2015	928.83 -	928.83	593.31	- 06/2015	06/2015	-	0/0
1024	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH , PPP (BOT)	05/2013	1,055.00 -	1,601.77	1,393.40	11/2015 -	-	-	0/0
1025	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH ,	06/2015	1,012.90 -	1,012.90	226.10	03/2016 -	-	-	0/0
1026	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH ,	03/2015	810.22 -	810.22	664.56	- 06/2015	06/2015	-	0/0
1027	FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH , PPP (BOT)	06/2015	1,583.79 -	1,583.79	1,568.11	01/2019 -	-	-	0/3
1028	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADHYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH , EPC	03/2015	511.83 -	511.83	240.05	08/2017 -	02/2020	30(O) -	0/0
1029	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH ,	08/2016	227.49 -	227.49	140.57	01/2019 -	08/2019	-	0/0
1030	FOUR LANNING BALANCE WORK FOR BHOPAL- BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH , Central Sector Projects	10/2017	639.97 -	639.97	274.24	10/2017 -	01/2020	27(O) -	0/0
1031	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	374.40 -	374.40	.00	09/2017 -	-	-	0/0
1032	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	990.61 -	990.61	17.41	09/2017 -	01/2021	40(O) -	0/4
1033	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH ,	12/2017	950.27 -	950.27	.00	- -	-	-	0/0
1034	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH ,	01/2018	960.24 -	960.24	328.34	- -	08/2020	- -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1035	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI,MADHYA PRADESH ,	01/2018	770.73 -	770.73	.00	-	-	-	0/0
1036	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]PWD,MADHYA PRADESH ,	03/2018	162.56 -	162.56	88.47	03/2018 -	12/2019	21(O) -	0/0
1037	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]PWD,MADHYA PRADESH ,	03/2018	166.21 -	166.21	30.52	08/2018 -	06/2020	22(O) -	0/0
1038	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]PWD,MADHYA PRADESH ,	02/2018	169.63 -	169.63	9.35	03/2018 -	07/2020	28(O) -	0/0
1039	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]PWD,MADHYA PRADESH ,	11/2017	235.91 -	235.91	117.24	02/2018 -	11/2019	21(O) -	0/0
1040	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]PWD,MADHYA PRADESH ,	11/2017	184.62 -	184.62	55.27	02/2018 -	11/2019	21(O) -	0/0
1041	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884]PWD,MADHYA PRADESH ,	03/2018	191.21 -	191.21	72.02	11/2019 -	11/2019	0(O) -	0/0
1042	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]PWD,MADHYA PRADESH ,	01/2017	205.05 -	205.05	73.22	03/2017 -	06/2020	39(O) -	0/0
1043	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]PWD,MADHYA PRADESH ,	03/2018	214.69 -	214.69	23.06	03/2018 -	11/2019	20(O) -	0/0
1044	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]PWD,MADHYA PRADESH ,	03/2018	217.22 -	217.22	20.43	08/2018 -	06/2020	22(O) -	0/0
1045	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]PWD,MADHYA PRADESH ,	03/2018	233.04 -	233.04	95.28	03/2018 -	11/2019	20(O) -	0/0
1046	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]PWD,MADHYA PRADESH ,	11/2017	249.05 -	249.05	118.29	07/2018 -	01/2020	18(O) -	0/0
1047	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]PWD,MADHYA PRADESH ,	11/2017	254.17 -	254.17	139.86	02/2018 -	11/2019	21(O) -	0/0
1048	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]PWD,MADHYA PRADESH ,	02/2018	279.44 -	279.44	76.00	03/2018 -	04/2020	25(O) -	0/0
1049	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 - [N24000895]PWD,MADHYA PRADESH ,	09/2016	287.34 -	287.34	148.65	01/2019 -	11/2019	10(O) -	0/0
1050	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]PWD,MADHYA PRADESH ,	01/2017	373.82 -	373.82	116.34	09/2019 -	05/2020	8(O) -	0/0
1051	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]PWD,MADHYA PRADESH ,	01/2016	809.16 -	809.16	219.42	07/2018 -	02/2020	19(O) -	0/0
1052	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]PWD,MADHYA PRADESH ,	03/2016	877.79 -	877.79	436.12	06/2019 -	11/2019	5(O) -	0/0
1053	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 - [N24000962]PWD,MADHYA PRADESH ,	09/2016	178.23 -	178.23	114.16	09/2018 -	08/2019	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1054	ANJANGAON TO MAH/MP BORDER - [N24001007]MORTH,MADHYA PRADESH ,	01/2017	359.00 359.00	359.00	182.80	06/2019 -	-	-	0/4
1055	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]PWD,MADHYA PRADESH ,	11/2017	392.33 -	392.33	242.88	03/2018 -	11/2019	20(O) -	0/0
1056	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]MORTH,MADHYA PRADESH ,	01/2019	264.50 -	264.50	.00	03/2021 -	03/2021	0(O) -	0/0
1057	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI,MADHYA PRADESH ,	10/2019	743.88 -	743.88	.00	- -	-	-	0/0
1058	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA , PPP (BOT)	10/2010	1,724.55 -	1,724.55	2,387.46	03/2013 -	12/2019	81(O) -	0/0
1059	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA , PPP (BOT)	05/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	-	-	2/2
1060	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA , EPC	03/2015	168.30 -	168.30	52.00	- -	-	-	0/4
1061	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA , EPC	08/2014	187.79 -	187.79	76.62	07/2016 -	-	-	0/12
1062	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA , EPC	01/2014	446.77 -	446.77	259.50	- -	-	-	3/4
1063	WIDENING NH-848 FROM KM 16.000 TO 34.000 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA , EPC	10/2015	289.60 -	289.60	90.65	- -	-	-	0/0
1064	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA , ITEM RATE	12/2011	156.26 227.00	247.95	175.00	- -	-	-	0/0
1065	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA , EPC	01/2015	225.81 -	225.81	85.11	- -	-	-	0/0
1066	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	2,288.18 -	2,288.18	487.81	05/2019 -	-	-	0/0
1067	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA ,	09/2015	414.51 -	414.00	531.36	05/2018 03/2019	05/2020	24(O) -1	0/0
1068	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA ,	10/2015	531.13 -	727.00	421.65	05/2018 -	09/2020	28(O) -	0/0
1069	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA , EPC	07/2015	1,885.74 -	1,885.74	1,636.02	05/2019 -	-	-	0/0
1070	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA ,	10/2015	593.26 41.54	636.24	438.73	05/2018 06/2020	06/2020	25(O) -6	0/1

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1071	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB SERVICE ROADS FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA ,	12/2015	649.50 -	649.50	134.58	03/2019 04/2021	04/2021	25(O) 0	0/0
1072	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA ,	08/2015	505.00 -	504.00	220.70	05/2018 04/2019	09/2020	28(O) 0	0/1
1073	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA , PPP (BOT)	01/2015	972.50 -	972.50	1,492.00	07/2017 -	10/2019	27(O) -	0/0
1074	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA , PPP (BOT)	06/2014	923.04 -	923.04	755.97	11/2016 -	05/2020	42(O) -	0/0
1075	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA ,	09/2005	168.00 -	168.00	226.24	06/2006 -	-	-	0/0
1076	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	1,871.34 67.34	1,871.34	3,495.79	01/2018 12/2018	12/2019	23(O) 1	0/0
1077	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA ,	04/2010	1,170.52 -	1,170.52	2,051.36	06/2012 -	-	-	0/0
1078	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA ,	03/2016	197.69 -	197.69	22.27	07/2018 -	-	-	0/0
1079	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA ,	03/2016	546.00 -	546.00	269.67	07/2019 12/2020	12/2020	17(O) 0	0/0
1080	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA ,	03/2016	591.66 -	591.66	310.56	07/2019 12/2020	12/2020	17(O) 0	0/0
1081	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA ,	03/2016	1,142.62 -	1,142.62	726.85	- -	-	-	0/0
1082	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA ,	03/2016	1,101.58 -	1,101.58	.00	- -	-	-	0/0
1083	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA ,	11/2016	1,071.61 -	1,071.61	365.61	- -	07/2021	- -	1/4
1084	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA ,	11/2016	1,064.88 -	1,064.88	.00	- -	07/2021	- -	0/4
1085	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA ,	11/2016	400.25 -	400.25	64.89	03/2019 -	02/2021	23(O) -	0/0
1086	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA ,	11/2016	446.17 -	446.17	38.97	03/2019 -	03/2021	24(O) -	0/0
1087	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA ,	11/2016	290.73 315.00	315.00	215.98	- 03/2020	03/2019	-	0/0
1088	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA ,	01/2017	244.90 -	244.90	243.33	05/2019 -	12/2019	7(O) -	0/0
1089	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA ,	02/2017	904.16 911.07	904.16	817.58	02/2020 11/2017	05/2020	3(O) 0	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1090	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA ,	03/2017	247.02 -	157.49	21.89	03/2020 02/2021	02/2020	-1(O) 0	0/0
1091	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA ,	03/2017	744.64 -	982.00	.00	03/2020 -	03/2020	0(O) -	0/0
1092	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA ,	03/2017	1,030.44 -	1,065.51	1,027.16	03/2020 -	05/2020	2(O) -	0/0
1093	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA ,	03/2017	988.34 -	1,043.28	1,094.73	03/2020 -	08/2020	5(O) -	0/0
1094	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA ,	03/2017	1,059.73 1,071.00	1,071.00	549.63	03/2017 05/2018	11/2020	44(O) 0	0/0
1095	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA ,	03/2017	296.19 -	254.00	248.60	03/2020 -	09/2019	-6(O) -	0/0
1096	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA ,	03/2017	1,098.06 -	1,160.64	1,082.97	03/2020 -	08/2020	5(O) -	0/0
1097	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA ,	12/2017	404.94 448.18	448.18	102.43	- -	10/2020	- -	0/0
1098	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA ,	01/2018	607.00 -	607.00	120.17	- -	08/2021	- -	0/1
1099	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA ,	01/2018	621.00 565.02	621.00	303.91	- 10/2018	04/2021	- 0	2/3
1100	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA , EPC	03/2018	291.53 -	291.53	30.82	- 11/2020	11/2020	- 0	0/0
1101	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA , EPC	03/2018	289.21 -	289.21	27.22	- -	11/2020	- -	0/0
1102	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA ,	03/2018	1,162.92 -	1,162.92	14.29	- -	07/2021	- -	0/0
1103	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA ,	03/2018	642.13 -	807.00	302.29	- -	12/2020	- -	0/0
1104	SARSAM TO KOTHARI - [N24001002]MORTH,MAHARASHTRA ,	02/2016	545.64 -	545.64	65.01	07/2019 -	-	-	0/4
1105	AKOLA TO AKOT - [N24001003]MORTH,MAHARASHTRA ,	01/2017	313.95 -	313.95	37.05	06/2019 -	-	-	0/4
1106	AKOT TO ANJANGAON - [N24001006]MORTH,MAHARASHTRA ,	01/2017	245.77 246.00	245.77	182.98	06/2019 -	-	-	0/4
1107	KHAMGAON TO SHEGAON - [N24001009]MORTH,MAHARASHTRA ,	02/2017	203.21 203.00	203.21	102.79	05/2019 -	12/2019	7(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1108	SHEGAON TO DEORI PHATA - [N24001010]MORTH,MAHARASHTRA ,	02/2017	373.10 373.00	373.10	123.43	05/2019 -	12/2019	7(O) -	0/4
1109	MEHKAR TO CHIKALI - [N24001011]MORTH,MAHARASHTRA ,	02/2017	322.48 322.00	322.48	202.08	05/2019 -	-	-	0/4
1110	CHIKALI TO KHAMGAON - [N24001012]MORTH,MAHARASHTRA ,	02/2017	548.03 548.00	548.03	287.00	06/2019 -	10/2019	4(O) -	0/4
1111	DIGRAS DARWAH KARANJA - [N24001013]MORTH,MAHARASHTRA ,	01/2017	391.06 391.00	391.06	68.00	06/2019 -	06/2020	12(O) -	0/0
1112	NANDGAON TO MORSHI - [N24001014]MORTH,MAHARASHTRA ,	01/2017	385.87 386.00	385.87	203.75	06/2019 -	12/2019	6(O) -	0/0
1113	MORSHI TO ACHALPUR - [N24001015]MORTH,MAHARASHTRA ,	01/2017	341.16 341.00	341.16	153.29	06/2019 -	12/2019	6(O) -	0/0
1114	MORSHI TO MAH/MP BORDER - [N24001016]MORTH,MAHARASHTRA ,	01/2017	471.61 472.00	471.61	259.90	06/2019 -	-	-	0/0
1115	DAHEGAON TO KUHI - [N24001017]MORTH,MAHARASHTRA ,	01/2017	228.89 228.89	228.89	125.00	06/2019 -	-	-	3/4
1116	BHANDARA TO GHOTITOK - [N24001018]MORTH,MAHARASHTRA ,	01/2017	392.83 393.00	392.83	281.60	06/2019 -	-	-	0/0
1117	KATOL TO WARUD - [N24001019]MORTH,MAHARASHTRA ,	01/2017	463.62 664.00	463.62	257.34	06/2019 -	08/2019	-	0/4
1118	AMDIT TO SAONER - [N24001021]MORTH,MAHARASHTRA ,	01/2017	396.91 396.91	396.91	248.48	06/2019 -	08/2019	-	3/4
1119	WADI TO ASOLA - [N24001022]MORTH,MAHARASHTRA ,	01/2017	363.82 363.82	363.82	41.10	09/2019 -	09/2020	12(O) -	1/4
1120	NAGAJ TO VAJAPUR - [N24001023]MORTH,MAHARASHTRA ,	01/2017	376.72 377.00	376.72	168.81	06/2019 -	12/2019	6(O) -	0/4
1121	MANGAON TO DIGHI PORT - [N24001024]MORTH,MAHARASHTRA ,	01/2017	457.52 457.52	457.52	202.98	07/2019 -	07/2020	12(O) -	2/4
1122	INDAPUR TO AGARDANDA - [N24001025]MORTH,MAHARASHTRA ,	01/2017	355.17 355.17	355.17	164.87	07/2019 -	12/2019	5(O) -	3/4
1123	WAKAN PALI KHOPOLI - [N24001026]MORTH,MAHARASHTRA ,	01/2017	376.19 376.19	376.19	29.03	05/2019 -	05/2020	12(O) -	1/4
1124	SHAHNUR PATGAON SECTION I - [N24001027]MORTH,MAHARASHTRA ,	01/2018	150.79 150.79	150.79	21.42	12/2019 -	12/2019	0(O) -	1/4
1125	PATGAON KHOPOLI SECTION I - [N24001028]MORTH,MAHARASHTRA ,	01/2018	170.00 -	170.00	39.57	12/2019 -	12/2019	0(O) -	0/4
1126	AHMADPUR TO PIMPLA - [N24001029]MORTH,MAHARASHTRA ,	01/2017	422.38 422.38	422.38	169.58	08/2019 -	08/2019	-	2/4
1127	PIMPLA TO MANJARUMBHA - [N24001030]MORTH,MAHARASHTRA ,	01/2017	595.77 595.77	595.77	132.44	08/2019 -	08/2019	-	2/4
1128	MANJUSUMBA TO CHUMBALI - [N24001031]MORTH,MAHARASHTRA ,	01/2017	228.54 228.54	228.54	99.30	08/2019 -	08/2019	-	2/4
1129	DEORI TO AMGAON - [N24001032]MORTH,MAHARASHTRA ,	01/2017	409.62 410.00	409.62	171.78	05/2019 -	05/2020	12(O) -	0/4
1130	MANTHA TALUKAS BORDER TO PARTUR - [N24001033]MORTH,MAHARASHTRA ,	01/2017	486.19 486.19	486.19	215.29	07/2019 -	07/2019	-	2/4
1131	PARTUR TO MAJALGAON - [N24001034]MORTH,MAHARASHTRA ,	01/2017	420.57 420.57	420.57	215.39	07/2019 -	07/2019	-	2/4
1132	MANSAR TO SALAIKHURD - [N24001035]MORTH,MAHARASHTRA ,	01/2018	418.36 -	418.36	116.13	12/2019 -	12/2019	0(O) -	0/4

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1133	MAJALGAON TO KAIJ - [N24001036]MORTH,MAHARASHTRA ,	01/2017	413.99 -	413.99	299.33	07/2019 -	07/2019	-	0/0
1134	KAIJ TO KUSALAM - [N24001037]MORTH,MAHARASHTRA ,	01/2017	554.78 554.78	554.78	159.90	07/2019 -	07/2019	-	2/4
1135	MAHAD TO RAIGAD FORT - [N24001038]MORTH,MAHARASHTRA ,	07/2018	237.40 -	237.40	8.34	05/2020 -	05/2020	0(O) -	0/4
1136	JINTUR TO PARBHANI - [N24001039]MORTH,MAHARASHTRA ,	01/2017	356.66 356.66	356.66	35.88	- -	-	-	0/4
1137	JAHIRABAD TO LATUR - [N24001040]MORTH,MAHARASHTRA ,	01/2017	461.96 461.96	461.96	151.43	11/2019 -	11/2019	0(O) -	2/4
1138	SHIROD SHAHPURER TO NANDED - [N24001041]MORTH,MAHARASHTRA ,	01/2017	211.34 211.34	211.34	101.83	07/2019 -	07/2019	-	2/4
1139	SALAIKHURD TO TIRORA - [N24001042]MORTH,MAHARASHTRA ,	01/2018	415.25 415.25	415.25	82.22	12/2019 -	12/2019	0(O) -	0/4
1140	NILAJPHATA TO BHANDARA - [N24001043]MORTH,MAHARASHTRA ,	01/2018	420.63 421.00	420.63	17.60	05/2020 -	05/2020	0(O) -	0/4
1141	KALMAB TO RALEGAON - [N24001044]MORTH,MAHARASHTRA ,	01/2017	467.78 -	467.78	294.91	06/2019 -	-	-	0/4
1142	JALGAON TO BHADGAON - [N24001045]MORTH,MAHARASHTRA ,	01/2018	307.54 308.00	307.54	124.59	11/2019 -	11/2019	0(O) -	0/4
1143	RALEGAON TO RAMTIRTH - [N24001046]MORTH,MAHARASHTRA ,	01/2017	210.81 -	210.81	106.69	07/2019 -	-	-	0/4
1144	BHADGAON TO CHALISGAON - [N24001047]MORTH,MAHARASHTRA ,	01/2018	259.55 260.00	259.55	145.00	11/2019 -	11/2019	0(O) -	0/0
1145	MEHKAR TO AJISPUR - [N24001048]MORTH,MAHARASHTRA ,	01/2017	232.77 -	232.77	85.51	07/2019 -	-	-	0/0
1146	KARAD TO VITA - [N24001049]MORTH,MAHARASHTRA ,	01/2018	344.85 245.00	344.85	68.04	12/2019 -	12/2019	0(O) -	0/4
1147	VITA TO NAGAJ - [N24001050]MORTH,MAHARASHTRA ,	03/2018	304.58 305.00	304.58	9.16	12/2019 -	12/2019	0(O) -	0/4
1148	NALDURG TO AKKALKOT - [N24001051]MORTH,MAHARASHTRA ,	02/2018	274.50 275.00	274.50	61.39	12/2019 -	12/2019	0(O) -	0/4
1149	SANGOLA TO JATH - [N24001052]MORTH,MAHARASHTRA ,	01/2018	257.38 257.00	257.38	61.15	12/2019 -	12/2019	0(O) -	0/4
1150	KARAD TO TAGAON - [N24001053]MORTH,MAHARASHTRA ,	01/2017	537.81 538.00	537.81	85.97	06/2019 -	06/2020	12(O) -	0/4
1151	TASGAON TO SHIRDHON - [N24001054]MORTH,MAHARASHTRA ,	01/2017	195.64 196.00	195.64	169.73	11/2019 -	11/2019	0(O) -	0/4
1152	HELWAK TO KARAD - [N24001055]MORTH,MAHARASHTRA ,	02/2017	416.99 -	416.99	113.40	07/2019 -	-	-	0/4
1153	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MORTH,MAHARASHTRA ,	02/2017	422.02 422.00	422.02	238.01	07/2019 -	-	-	0/0
1154	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MORTH,MAHARASHTRA ,	02/2017	407.19 407.00	407.19	25.00	06/2019 -	06/2020	12(O) -	0/4
1155	KARWANDI TO RAJURI - [N24001058]MORTH,MAHARASHTRA ,	03/2018	276.95 277.00	276.95	81.47	12/2019 -	12/2019	0(O) -	0/4
1156	SHIVUR TO YEOLA - [N24001059]MORTH,MAHARASHTRA ,	03/2018	181.08 -	181.08	2.50	12/2019 -	12/2019	0(O) -	0/4
1157	PALPHATA TO PHULAMBARI - [N24001060]MORTH,MAHARASHTRA ,	03/2018	227.19 227.00	227.19	60.23	12/2019 -	12/2019	0(O) -	0/4

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1158	CHIKALI TO DHAD - [N24001061]MORTH,MAHARASHTRA ,	03/2018	189.46 189.00	189.46	21.54	12/2019 -	12/2019	0(O) -	0/4
1159	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]MORTH,MAHARASHTRA ,	03/2018	336.21 336.00	336.21	64.66	12/2019 -	12/2019	0(O) -	0/4
1160	WADIGODRI TO DHANGRIIMPRI - [N24001063]MORTH,MAHARASHTRA ,	03/2018	194.23 194.00	194.23	68.23	02/2020 -	02/2020	0(O) -	0/4
1161	DHANGRIIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]MORTH,MAHARASHTRA ,	03/2018	217.14 217.00	217.14	66.77	02/2020 -	02/2020	0(O) -	0/4
1162	PARBHANI TO GANGKHED - [N24001065]MORTH,MAHARASHTRA ,	03/2018	238.19 238.00	238.19	40.85	12/2019 -	12/2019	0(O) -	0/4
1163	LATUR TO PANGAON - [N24001066]MORTH,MAHARASHTRA ,	03/2018	336.47 336.00	336.47	109.48	12/2019 -	12/2019	0(O) -	0/4
1164	OMREGA TO AUSA - [N24001067]MORTH,MAHARASHTRA ,	03/2018	272.04 272.00	272.04	124.24	12/2019 -	12/2019	0(O) -	0/4
1165	WASHIM TO DASTAPUR - [N24001068]MORTH,MAHARASHTRA ,	03/2018	165.51 -	165.51	35.45	12/2019 -	12/2019	0(O) -	1/4
1166	NANDED TO JALKOT - [N24001069]MORTH,MAHARASHTRA ,	12/2017	456.93 457.00	456.93	54.50	09/2019 -	09/2019	0(O) -	1/4
1167	DASTAPUR TO KARANJA - [N24001070]MORTH,MAHARASHTRA ,	03/2018	182.63 -	182.63	83.40	12/2019 -	12/2019	0(O) -	2/4
1168	JALKOT TO TOGRI - [N24001071]MORTH,MAHARASHTRA ,	07/2018	299.92 300.00	299.92	4.20	08/2020 -	08/2020	0(O) -	0/4
1169	KHERDA TO NAGZARI - [N24001072]MORTH,MAHARASHTRA ,	03/2018	181.30 -	181.30	70.50	12/2019 -	12/2019	0(O) -	0/4
1170	KOTHARI TO DHANORA - [N24001073]MORTH,MAHARASHTRA ,	09/2018	301.38 301.00	301.38	41.00	08/2020 -	08/2020	0(O) -	0/0
1171	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MORTH,MAHARASHTRA ,	03/2018	249.29 -	249.29	72.20	12/2019 -	12/2019	0(O) -	0/0
1172	OSMANNAGAR TO KUNDRAL - [N24001075]MORTH,MAHARASHTRA ,	09/2017	344.25 344.00	344.25	33.02	08/2020 -	08/2020	0(O) -	0/4
1173	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MORTH,MAHARASHTRA ,	03/2018	219.91 -	219.91	106.46	12/2019 -	12/2019	0(O) -	0/0
1174	KUNDRAL TO WAZAR - [N24001077]MORTH,MAHARASHTRA ,	01/2018	225.25 225.00	225.25	121.75	12/2019 -	12/2019	0(O) -	2/4
1175	PUNE TO MALE VILLAGE - [N24001078]MORTH,MAHARASHTRA ,	03/2018	228.31 -	228.31	13.50	12/2019 -	12/2019	0(O) -	0/0
1176	ARDHAPUR TO HIMAYATNAGAR - [N24001079]MORTH,MAHARASHTRA ,	12/2017	426.06 426.00	426.06	66.97	06/2020 -	06/2020	0(O) -	1/4
1177	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MORTH,MAHARASHTRA ,	03/2018	256.15 -	256.15	15.50	12/2019 -	12/2019	0(O) -	0/0
1178	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]MORTH,MAHARASHTRA ,	03/2018	294.87 295.00	294.87	12.30	12/2019 -	12/2019	0(O) -	1/4
1179	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MORTH,MAHARASHTRA ,	03/2018	223.46 -	223.46	21.42	12/2019 -	12/2019	0(O) -	0/0
1180	CHIKLI TO TAKARKHED - [N24001083]MORTH,MAHARASHTRA ,	03/2018	393.10 393.10	393.10	125.97	12/2019 -	12/2019	0(O) -	2/4
1181	PAHUR TO BODHWAD - [N24001084]MORTH,MAHARASHTRA ,	01/2017	244.93 -	244.93	40.23	05/2020 -	05/2020	0(O) -	0/4
1182	TAKARKHED TO JALNA - [N24001085]MORTH,MAHARASHTRA ,	09/2017	417.90 418.00	417.90	87.26	06/2019 -	12/2019	6(O) -	0/4

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1183	BODHWAD TO STATE BORDER - [N24001086]MORTH,MAHARASHTRA ,	01/2017	178.26 -	178.26	118.95	07/2019 -	-	-	0/4
1184	MANGRUPHIR TO MAHAN - [N24001087]MORTH,MAHARASHTRA ,	03/2018	222.13 222.13	222.13	60.36	11/2019 -	11/2019	0(O) -	0/4
1185	JALGAON TO NANDURA - [N24001088]MORTH,MAHARASHTRA ,	03/2018	177.84 177.00	177.84	125.69	12/2019 -	12/2019	0(O) -	0/0
1186	MALEGAON TO RISOD - [N24001089]MORTH,MAHARASHTRA ,	02/2018	303.24 303.24	303.24	107.97	12/2019 -	12/2019	0(O) -	0/4
1187	KOLDE TO KHETIYA - [N24001090]MORTH,MAHARASHTRA ,	01/2017	509.18 -	509.18	175.93	07/2019 -	-	-	0/4
1188	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIKA TO RENGAPALI ODISHA - [N24001091]MORTH,MAHARASHTRA ,	03/2016	536.65 356.00	536.65	42.25	12/2019 -	12/2019	0(O) -	0/0
1189	SATARA TO MHASWAD - [N24001092]MORTH,MAHARASHTRA ,	01/2017	653.46 -	653.46	202.42	07/2019 -	-	-	0/4
1190	ARNI TO NAIGAINBANDI - [N24001093]MORTH,MAHARASHTRA ,	12/2017	309.94 310.00	309.94	51.32	12/2019 -	12/2019	0(O) -	0/0
1191	NAIGAONBANDI TO MANGRULPIR - [N24001094]MORTH,MAHARASHTRA ,	12/2017	244.04 244.00	244.04	25.94	03/2019 -	12/2019	9(O) -	0/0
1192	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MORTH,MAHARASHTRA ,	01/2017	388.44 -	388.44	188.77	- -	-	-	0/0
1193	TALEGAON TO GONAPUR - [N24001096]MORTH,MAHARASHTRA ,	01/2018	264.41 264.00	264.41	32.71	03/2019 -	12/2019	9(O) -	0/0
1194	SELDOH TO PANVAR - [N24001097]MORTH,MAHARASHTRA ,	07/2018	404.33 404.00	404.33	30.19	05/2020 -	05/2020	0(O) -	0/4
1195	WARDHA TO HINGAGHAT - [N24001098]MORTH,MAHARASHTRA ,	01/2018	216.90 216.90	216.90	45.00	12/2019 -	12/2019	0(O) -	1/4
1196	MHASWAD TO TEMBHURNI - [N24001099]MORTH,MAHARASHTRA ,	01/2017	488.60 -	488.60	182.71	07/2019 -	-	-	0/4
1197	AHMEDNAGAR TO BARAMATI - [N24001100]MORTH,MAHARASHTRA ,	01/2017	955.40 -	955.40	338.50	08/2019 -	08/2019	-	0/4
1198	KURUDWADI TO PANDHARPUR - [N24001101]MORTH,MAHARASHTRA ,	01/2017	307.63 -	307.63	148.17	07/2019 -	-	-	0/4
1199	PANDHARPUR TO SANGOLA - [N24001102]MORTH,MAHARASHTRA ,	07/2017	218.38 -	218.38	168.75	07/2019 -	-	-	0/4
1200	SARAD VANI PIMPALGAON - [N24001103]MORTH,MAHARASHTRA ,	01/2017	250.46 -	250.46	103.63	07/2019 -	-	-	0/4
1201	MALEWADA TO CHIMUR - [N24001104]MORTH,MAHARASHTRA ,	10/2016	322.55 -	322.55	156.91	06/2019 -	06/2020	12(O) -	2/4
1202	CHIMUR TO WARORA - [N24001105]MORTH,MAHARASHTRA ,	11/2016	467.70 -	467.70	146.72	03/2019 -	-	-	0/4
1203	PEN TO KHOPOLI - [N24001106]MORTH,MAHARASHTRA ,	03/2018	301.39 302.00	301.39	.00	03/2018 -	12/2019	21(O) -	0/4
1204	PANCHARAL TO MANDANGHAR - [N24001107]MORTH,MAHARASHTRA ,	07/2018	381.08 302.00	381.08	13.00	05/2020 -	05/2020	0(O) -	0/4
1205	CHALISGAON TO NANDGAON - [N24001108]MORTH,MAHARASHTRA ,	03/2018	206.97 207.00	206.97	78.89	12/2019 -	12/2019	0(O) -	0/4
1206	KUSUMBA TO MALEGAON - [N24001109]MORTH,MAHARASHTRA ,	03/2018	243.45 244.00	243.45	67.02	12/2019 -	12/2019	0(O) -	0/4

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1207	BAMNI TO NAVEGAON - [N24001110]MORTH,MAHARASHTRA ,	09/2017	241.69 242.00	241.69	146.29	04/2020 -	04/2020	0(O) -	1/4
1208	KOLHA TO NASRATPUR - [N24001111]MORTH,MAHARASHTRA ,	04/2016	281.78 282.00	281.78	47.73	04/2019 -	04/2020	12(O) -	0/4
1209	NASRATPUR TO BARASGAON - [N24001112]MORTH,MAHARASHTRA ,	07/2016	406.54 406.54	406.54	142.00	09/2019 -	09/2019	0(O) -	2/4
1210	BARASGAON TO RAHATEE - [N24001113]MORTH,MAHARASHTRA ,	07/2016	289.11 290.00	289.11	148.00	09/2018 -	04/2021	31(O) -	0/4
1211	INDAPUR TO VADPALE - [N24001114]MORTH,MAHARASHTRA ,	01/2017	1,202.52 1,202.52	1,202.52	635.90	12/2019 -	03/2020	3(O) -	1/4
1212	VADPALE TO BHOGAN KHURD - [N24001115]MORTH,MAHARASHTRA ,	01/2017	1,598.47 1,598.47	1,598.47	751.91	11/2019 -	03/2020	4(O) -	1/4
1213	GADCHIROLI TO MUL - [N24001116]MORTH,MAHARASHTRA ,	12/2016	484.15 -	484.15	160.31	06/2019 -	-	-	2/4
1214	MUL TO CHANDRAPUR - [N24001117]MORTH,MAHARASHTRA ,	12/2016	162.34 -	162.34	32.80	07/2019 -	07/2019	-	1/4
1215	SAKOLI TO BHANDARA - [N24001118]MORTH,MAHARASHTRA ,	01/2017	362.96 362.96	362.96	37.83	06/2019 -	11/2019	5(O) -	0/4
1216	NAGBHID TO ARMORI - [N24001119]MORTH,MAHARASHTRA ,	09/2016	269.05 -	269.05	197.91	07/2019 -	-	-	0/4
1217	AKKALKOT TO DHUDHNI - [N24001120]MORTH,MAHARASHTRA ,	04/2016	211.42 -	211.42	131.85	02/2019 -	02/2020	12(O) -	0/4
1218	NASHIK TO PETH - [N24001121]MORTH,MAHARASHTRA ,	12/2015	289.60 -	289.60	118.81	11/2018 -	11/2019	12(O) -	0/4
1219	PAITHAN TO SHIRUR - [N24001122]MORTH,MAHARASHTRA ,	03/2017	341.80 -	341.80	117.89	06/2019 -	-	-	0/4
1220	SHIRUR TO KHARDA - [N24001123]MORTH,MAHARASHTRA ,	02/2017	381.77 -	381.77	100.79	06/2019 -	-	-	0/4
1221	AURANGABAD TO SILLOD - [N24001124]MORTH,MAHARASHTRA ,	02/2017	456.32 -	456.32	91.75	06/2019 -	-	-	0/4
1222	SILLOD TO FARDAPUR - [N24001125]MORTH,MAHARASHTRA ,	02/2017	337.46 -	337.46	39.22	06/2019 -	-	-	0/4
1223	FARDAPUR TO JALGAON - [N24001126]MORTH,MAHARASHTRA ,	02/2017	456.45 -	456.45	56.74	06/2019 -	-	-	0/4
1224	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MORTH,MAHARASHTRA ,	02/2017	406.51 -	406.51	281.03	06/2019 -	-	-	0/0
1225	BHOKAR TO SARSAM - [N24001128]MORTH,MAHARASHTRA ,	02/2017	295.09 -	295.99	162.64	07/2019 -	-	-	0/4
1226	BHOGAN KHURD TO KASHEDI - [N24001132]MORTH,MAHARASHTRA ,	09/2017	743.21 743.21	743.21	131.87	06/2021 -	06/2021	0(O) -	1/4
1227	PARSHURAM GHAT TO ARAWALI - [N24001133]MORTH,MAHARASHTRA ,	04/2016	983.14 983.14	983.14	655.15	12/2019 -	11/2019	-1(O) -	1/4
1228	KANTE TO WAKED - [N24001134]MORTH,MAHARASHTRA ,	03/2016	1,230.02 1,230.02	1,230.02	500.61	11/2019 -	11/2019	0(O) -	1/4
1229	WAKED TO TALEGAON - [N24001135]MORTH,MAHARASHTRA ,	02/2016	1,244.75 1,245.00	1,244.75	357.60	02/2019 -	-	-	0/0
1230	TALGAON TO KALMATH - [N24001136]MORTH,MAHARASHTRA ,	10/2016	904.70 904.70	904.70	604.05	03/2020 -	03/2020	0(O) -	2/4
1231	KALMATH TO ZARAP - [N24001137]MORTH,MAHARASHTRA ,	09/2016	1,338.13 1,338.13	1,338.13	959.51	03/2020 -	03/2020	0(O) -	3/5

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1232	PARLI PIMPLA DAHIGUDA - [N24001138]MORTH,MAHARASHTRA ,	02/2017	205.72 205.72	205.72	30.42	06/2019 -	06/2020	12(O) -	1/4
1233	RISOD TO HINGOLI - [N24001149]MORTH,MAHARASHTRA ,	02/2018	355.99 355.99	355.99	112.97	12/2019 -	12/2019	0(O) -	0/0
1234	WARDHA TO ARVI - [N24001150]MORTH,MAHARASHTRA ,	02/2018	313.58 313.58	313.58	4.96	04/2020 -	04/2020	0(O) -	0/4
1235	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL,MANIPUR ,	08/2017	517.57 -	457.77	137.04	10/2018 -	10/2021	36(O) -	1/4
1236	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. - [N24001174]PWD,MANIPUR ,	10/2016	235.31 -	235.31	91.38	11/2020 -	11/2020	0(O) -	0/0
1237	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA ,	12/2015	479.20 -	479.20	711.38	05/2018 03/2018	10/2019	17(O) -2	0/0
1238	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA ,	04/2017	553.51 -	553.51	27.90	- -	09/2021	- -	0/4
1239	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA ,	03/2019	306.28 -	306.28	42.66	05/2019 -	-	-	0/0
1240	WIDENING TO 2 LANE RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM , ITEM RATE	11/2010	624.41 -	992.67	853.82	03/2011 -	12/2019	105(O) -	0/0
1241	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM , ITEM RATE	08/2010	193.69 -	327.92	254.24	10/2010 -	12/2019	110(O) -	0/0
1242	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM , ITEM RATE	08/2010	195.04 -	377.99	305.38	10/2010 -	06/2020	116(O) -	0/0
1243	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM ,	04/2017	519.09 -	519.09	.00	09/2019 -	09/2019	0(O) -	0/0
1244	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM ,	04/2017	640.07 -	640.07	.00	09/2019 -	09/2019	0(O) -	0/0
1245	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM ,	04/2017	642.96 -	642.96	.00	09/2019 -	09/2019	0(O) -	0/0
1246	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM ,	04/2017	473.18 -	473.18	.00	09/2019 -	09/2019	0(O) -	0/0
1247	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM ,	04/2017	537.82 -	537.82	.00	09/2019 -	09/2019	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1248	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM ,	04/2017	518.53 -	518.53	.00	09/2019 -	09/2019	0(O) -	0/0
1249	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM ,	04/2017	404.29 -	404.29	.00	09/2019 -	09/2019	0(O) -	0/0
1250	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM ,	04/2017	428.11 -	428.11	.00	09/2019 -	09/2019	0(O) -	0/0
1251	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]PWD,MIZORAM ,	08/2010	186.96 -	305.61	275.06	09/2014 -	12/2019	63(O) -	0/0
1252	GWALIOR-JHANSI NH-75 - [N24000089]NHAI,MULTI STATE , PPP (ANNUITY)	12/2003	604.00 -	604.00	423.83	12/2009 -	08/2020	128(O) -	0/0
1253	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE , PPP (BOT)	02/2009	1,693.75 2,848.49	1,693.75	2,848.49	08/2011 -	-	-	2/2
1254	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE , PPP (ANNUITY)	02/2011	2,498.76 -	2,498.76	2,531.46	08/2014 -	-	-	0/0
1255	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE , PPP (BOT)	09/2011	2,848.00 -	2,848.00	1,159.10	03/2014 -	12/2019	69(O) -	0/0
1256	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE , PPP (BOT)	09/2011	754.00 -	754.00	1,364.18	03/2013 -	12/2019	81(O) -	0/0
1257	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE , PPP (BOT)	10/2012	1,928.22 -	2,945.00	3,070.11	04/2015 -	-	-	0/0
1258	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,MULTI STATE ,	09/2015	788.51 -	788.51	103.37	03/2018 -	-	-	0/0
1259	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE ,	09/2016	1,244.10 -	1,244.10	1,335.00	-	02/2020	-	0/0
1260	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE ,	03/2018	1,294.47 -	1,296.00	.00	-	-	-	0/0
1261	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE ,	03/2018	998.70 -	962.00	.00	-	-	-	0/0
1262	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD MON-TAMLU-MERANGKONG ROAD PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND , ITEM RATE	12/2010	1,296.00 -	1,296.00	.00	02/2011 -	-	-	0/0
1263	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND ,	03/2016	373.07 387.00	373.07	209.22	08/2016 -	08/2019	-	2/4
1264	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND ,	03/2016	396.52 339.55	396.52	234.03	08/2016 -	06/2020	46(O) -	2/4

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1265	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND ,	03/2016	429.52 340.00	429.52	166.55	08/2016 -	08/2019	-	2/4
1266	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND ,	02/2017	507.68 -	507.68	129.13	04/2017 -	-	-	1/4
1267	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND ,	02/2017	387.00 -	387.00	135.12	09/2018 -	-	-	1/4
1268	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND ,	03/2018	500.09 -	500.09	.00	09/2018 -	-	-	0/0
1269	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND ,	03/2018	339.57 233.35	339.57	.00	09/2018 07/2019	-	-	0/0
1270	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND ,	03/2018	239.30 -	239.30	.00	09/2018 05/2019	-	-	0/4
1271	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND ,	03/2018	285.68 -	285.68	.00	09/2018 -	-	-	0/4
1272	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND ,	03/2018	315.03 -	315.03	4.38	09/2018 -	-	-	0/2
1273	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND ,	03/2018	240.64 -	240.64	2.11	09/2018 -	-	-	0/2
1274	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND ,	03/2018	237.72 136.73	237.72	21.71	09/2018 11/2018	-	-	1/2
1275	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND ,	03/2018	251.97 160.10	251.97	16.63	09/2018 11/2018	-	-	0/2
1276	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND ,	03/2018	282.98 -	282.98	12.76	09/2018 11/2018	-	-	0/2
1277	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND ,	03/2018	215.12 -	215.12	10.07	09/2018 -	-	-	1/2
1278	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND ,	03/2018	215.79 -	215.79	.00	09/2018 -	-	-	1/2

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1279	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND ,	03/2018	272.89 -	272.89	.00	09/2018 -	-	-	0/0
1280	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND ,	03/2018	323.98 -	323.98	.00	09/2018 -	-	-	0/0
1281	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]PWD,NAGALAND ,	10/2016	167.62 -	167.62	42.15	12/2020 -	12/2020	0(O) -	0/0
1282	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]PWD,NAGALAND ,	10/2016	172.63 -	172.63	45.02	12/2020 -	12/2020	0(O) -	0/0
1283	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]PWD,NAGALAND ,	11/2016	336.25 369.96	336.25	62.64	09/2019 -	09/2019	0(O) -	0/0
1284	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]PWD,NAGALAND ,	03/2017	217.35 -	217.35	35.10	11/2020 -	11/2020	0(O) -	0/0
1285	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- [N24001180]PWD,NAGALAND ,	03/2019	237.51 -	237.51	.00	12/2022 -	12/2022	0(O) -	0/0
1286	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA , PPP (BOT)	03/2012	1,410.00 -	1,410.00	1,935.14	09/2014 -	-	-	0/0
1287	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA , PPP (BOT)	12/2011	1,047.00 -	1,047.00	1,874.43	06/2014 -	03/2019	-	0/0
1288	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA , EPC	01/1991	218.63 -	218.63	29.27	10/2017 -	-	-	0/0
1289	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA ,	01/1991	229.41 -	229.41	6.65	05/2018 -	-	-	0/0
1290	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA , EPC	07/2014	342.05 -	342.05	258.91	01/2017 -	-	-	0/0
1291	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA ,	07/2015	1,282.94 -	1,282.94	210.80	- -	04/2020	- -	0/0
1292	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA ,	12/2015	752.28 -	752.28	.00	- -	11/2019	- -	0/0
1293	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA , EPC	12/2011	159.39 -	159.39	210.29	11/2017 -	09/2019	22(O) -	0/0
1294	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA , EPC	12/2011	191.08 -	191.08	99.98	08/2015 -	12/2019	52(O) -	0/0
1295	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA ,	02/2016	1,069.65 -	1,069.65	502.75	- -	03/2020	- -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1296	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA ,	09/2016	2,510.04 -	2,510.04	252.10	08/2019 -	03/2021	19(O) -	0/0
1297	REHABILITATION AND UPGRADATION TO FOUR LANE OF BINJHABAHAL TO TELEBANI SECTION KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA ,	10/2016	1,008.96 -	1,008.96	469.78	- -	03/2021	- -	0/0
1298	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA ,	03/2014	191.50 192.00	192.00	136.19	05/2016 -	12/2019	43(O) -	0/0
1299	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY W - [N24000640]MORTH,ODISHA ,	01/2015	326.63 327.00	326.63	249.26	04/2018 -	-	-	0/0
1300	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA ,	02/2015	239.91 240.00	160.00	147.25	10/2017 -	-	-	0/0
1301	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA ,	07/2014	342.05 342.00	342.00	258.91	01/2017 -	-	-	0/0
1302	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA ,	08/2013	171.96 172.00	172.00	88.30	06/2016 -	11/2019	41(O) -	0/0
1303	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA ,	06/2016	157.30 157.00	157.30	97.29	06/2018 -	-	-	0/0
1304	REHABILITATION AND UPGRADATION BY 4-LANE OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA ,	03/2017	1,288.07 -	1,420.00	365.00	03/2020 -	03/2021	12(O) -	0/0
1305	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA , Central Sector Projects	07/2017	476.56 -	476.56	.00	07/2017 11/2020	06/2021	47(O) 0	0/0
1306	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA ,	12/2017	686.65 -	686.65	80.87	- 07/2020	06/2021	- 0	0/0
1307	REHABILITATION AND UPGRADATION OF FOUR LANE OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA ,	12/2017	417.51 -	417.51	8.42	- -	06/2021	- -	0/0
1308	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA ,	01/2018	953.09 -	953.09	109.21	- 05/2020	06/2021	- 0	0/0
1309	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA ,	01/2018	668.86 -	668.86	109.20	- 05/2020	06/2021	- 0	0/0
1310	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA ,	01/2018	633.68 -	633.68	.00	- -	-	-	0/0
1311	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA ,	01/2018	614.48 -	614.48	31.00	- -	08/2021	- -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1312	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA ,	01/2018	564.66 -	564.66	21.00	- -	08/2021	- -	0/0
1313	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA ,	01/2018	686.65 -	686.65	75.79	- 03/2020	06/2021	- 0	0/0
1314	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM - [N24000737]NHAI,ODISHA ,	01/2018	1,522.00 -	1,522.00	.00	- -	-	-	0/0
1315	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA ,	01/2018	999.00 -	999.00	.00	- -	-	-	0/0
1316	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA ,	01/2018	503.88 -	503.88	.00	- -	06/2021	- -	0/0
1317	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA , EPC	03/2018	806.11 -	806.11	6.78	- -	04/2021	- -	0/0
1318	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26. - [N24000911]MORTH,ODISHA ,	03/2016	165.06 -	165.06	92.59	12/2016 -	-	-	0/0
1319	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MORTH,ODISHA ,	08/2016	287.70 -	287.70	153.90	02/2017 -	-	-	0/0
1320	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MORTH,ODISHA ,	09/2016	295.67 -	295.67	127.75	02/2017 -	-	-	0/0
1321	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MORTH,ODISHA ,	12/2016	223.50 -	223.50	44.52	08/2018 -	-	-	0/0
1322	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MORTH,ODISHA ,	12/2016	206.88 -	206.88	41.69	04/2018 -	-	-	0/0
1323	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MORTH,ODISHA ,	03/2018	214.23 -	214.23	23.44	08/2018 -	-	-	0/0
1324	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MORTH,ODISHA ,	03/2018	199.16 -	199.16	25.63	08/2018 -	-	-	0/0
1325	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB , EPC	12/2015	766.36 -	766.36	666.72	- 09/2019	-	-	0/0
1326	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB , EPC	11/2015	847.02 -	847.02	1,086.49	- 09/2019	-	-	0/0
1327	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB , EPC	11/2015	889.24 -	904.82	722.92	- 12/2019	-	-	0/0
1328	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB ,	09/2014	479.00 -	479.00	453.59	- -	03/2020	- -	0/0
1329	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB ,	10/2015	447.29 746.43	746.43	600.33	12/2017 06/2020	12/2019	24(O) 0	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1330	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB , EPC	06/2015	892.17 -	892.17	648.44	- -	-	-	0/0
1331	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB ,	08/2016	1,388.34 2,525.80	2,525.80	1,449.00	09/2019 03/2020	09/2019	0(O) 0	0/0
1332	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB ,	08/2016	1,169.61 1,367.00	1,169.61	1,063.10	- -	04/2020	- -	0/0
1333	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB ,	03/2017	754.54 -	756.27	159.58	03/2020 -	04/2020	1(O) -	0/0
1334	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB ,	02/2018	261.76 -	207.00	62.85	- -	01/2021	- -	0/0
1335	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB , EPC	03/2018	199.90 149.90	199.90	60.39	- -	-	-	0/0
1336	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB , EPC	03/2018	196.05 149.90	196.05	143.03	- -	01/2020	- -	0/0
1337	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905]PWD,PUNJAB ,	03/2018	322.48 -	322.48	48.73	07/2020 -	07/2020	0(O) -	0/0
1338	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906]PWD,PUNJAB ,	03/2018	173.24 -	173.24	10.97	06/2020 -	06/2020	0(O) -	0/0
1339	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]PWD,PUNJAB ,	03/2018	293.10 -	293.10	10.26	08/2020 -	08/2020	0(O) -	0/0
1340	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]PWD,PUNJAB ,	10/2017	1,069.59 -	1,069.59	629.87	10/2019 -	10/2019	0(O) -	0/0
1341	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0.000 - [N24000910]PWD,PUNJAB ,	03/2018	170.57 -	170.57	46.23	11/2020 -	11/2020	0(O) -	0/0
1342	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927]PWD,PUNJAB ,	03/2018	293.64 -	293.64	28.24	08/2020 -	08/2020	0(O) -	0/0
1343	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]PWD,PUNJAB ,	03/2018	293.64 -	293.64	28.24	08/2020 -	08/2020	0(O) -	0/0
1344	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN , EPC	10/2014	269.22 -	269.22	33.24	01/2015 -	-	-	0/0
1345	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN , EPC	10/2014	257.09 -	257.09	14.18	01/2015 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1346	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN , EPC	10/2013	278.87 -	278.87	.00	05/2014 -	-	-	0/0
1347	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN , ITEM RATE	01/1991	376.52 -	376.52	.00	04/2014 -	-	-	0/0
1348	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN , EPC	02/2015	383.40 -	383.40	224.68	03/2015 -	-	-	0/0
1349	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN , EPC	12/2015	621.43 -	621.43	387.00	06/2018 -	-	-	0/4
1350	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN ,	09/2014	425.19 -	425.19	276.40	09/2016 09/2014	10/2019	37(O) 0	0/0
1351	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN ,	10/2015	597.00 -	597.00	587.64	10/2017 04/2018	01/2020	27(O) 0	3/4
1352	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN , PPP (BOT)	11/2012	530.07 -	530.07	556.02	08/2016 -	12/2019	40(O) -	0/0
1353	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN , PPP (BOT)	08/2014	822.90 -	822.90	844.08	04/2018 -	-	-	0/0
1354	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	2,323.04	10/2013 -	-	-	0/0
1355	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	492.00	10/2013 -	-	-	0/4
1356	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN , PPP (BOT)	02/2008	1,673.70 -	1,673.70	3,326.93	10/2011 -	-	-	0/0
1357	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS - DHOLPUR - [N24000520]NHAI,RAJASTHAN ,	08/2015	275.90 -	275.90	257.52	- 02/2016	10/2019	- 0	0/0
1358	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI,RAJASTHAN , PPP (BOT)	06/2016	637.18 -	637.18	588.00	06/2019 -	09/2019	3(O) -	0/0
1359	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN , PPP (BOT)	06/2016	763.23 -	763.23	216.17	06/2019 -	11/2019	5(O) -	0/0
1360	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN ,	06/2016	649.00 -	649.00	296.30	06/2019 -	09/2019	3(O) -	0/0
1361	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN ,	07/2016	688.70 881.00	688.70	701.76	- 05/2017	11/2019	- 0	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1362	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN ,	07/2016	331.46 -	331.46	267.94	10/2018 -	-	-	0/0
1363	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN ,	08/2016	320.30 -	320.30	237.81	01/2019 -	10/2019	9(O) -	4/4
1364	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN ,	09/2016	1,239.82 -	1,239.82	1,280.27	- -	05/2020	- -	3/4
1365	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN ,	09/2016	1,100.19 -	1,100.19	900.00	- -	12/2019	- -	0/0
1366	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN ,	12/2016	1,031.95 -	1,031.95	367.00	- -	08/2020	- -	0/0
1367	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN ,	04/2017	894.00 -	894.00	730.00	04/2020 -	11/2019	-5(O) -	0/0
1368	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN , Central Sector Projects	10/2017	964.17 -	964.17	370.32	10/2017 -	11/2020	37(O) -	0/0
1369	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN ,	12/2017	1,308.73 -	1,308.73	99.68	- -	12/2020	- -	0/0
1370	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN ,	02/2018	1,103.88 -	1,103.88	267.65	- -	09/2020	- -	0/0
1371	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN ,	02/2018	741.86 -	741.86	.00	- -	-	-	0/0
1372	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN ,	02/2018	716.76 -	716.76	171.45	- -	-	-	0/0
1373	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN ,	03/2018	874.25 -	874.25	80.10	- -	-	-	0/0
1374	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN ,	03/2018	1,158.35 -	1,158.35	245.17	- -	-	-	0/0
1375	WIDENING STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950]PWD,RAJASTHAN ,	11/2017	187.82 -	187.82	53.11	04/2018 -	-	-	1/4
1376	NETRA VILLAGE TO MANDORE SECTION OF NH-65 KM 267+500 TO 296+070 (4L) UNDER EPC. - [N24000951]PWD,RAJASTHAN ,	10/2014	382.81 -	382.81	333.60	01/2015 -	-	-	3/4
1377	UP-GRADATION TO TWO LANE WITH PAVED SHOULDER FOR SECTION FROM KM 58.000 TO KM 91.600 (BALOTRA TO SAN - [N24000952]PWD,RAJASTHAN ,	01/2017	179.32 -	179.32	96.12	11/2017 -	-	-	2/4

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1378	CONSTRUCTION OF NAGPUR BYPASS FROM EXISTING KM 166/260 TO KM 180/500 OF NH-65 ON EPC MODE. - [N24000953]PWD,RAJASTHAN ,	03/2016	155.77 -	155.77	97.42	09/2016 -	-	-	3/4
1379	NAGPUR-BIKANER OF NH-11 (2L+PS) UNDER PPP. - [N24000954]PWD,RAJASTHAN ,	01/2012	378.07 478.73	478.73	188.98	01/2014 -	-	-	1/4
1380	CITTORGARH-NEEMACH (4L) OF NH-79 AND NIMBAHARA PRATAPGARH (2L+PS) OF NH-113 UNDER PPP. - [N24000955]PWD,RAJASTHAN ,	10/2012	511.21 -	511.21	814.79	10/2013 -	-	-	3/4
1381	DEVELOPMENT AND OPERATION OF BIKANER-SURATGARH SECTION OF NH-15 BY 2L+PS IN THE STATE OF RAJASTHAN - [N24000956]PWD,RAJASTHAN ,	03/2009	501.00 671.54	671.54	659.98	09/2013 -	-	-	3/4
1382	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709 - [N24000957]PWD,RAJASTHAN ,	11/2017	163.95 -	163.95	62.36	04/2018 -	-	-	3/4
1383	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000958]PWD,RAJASTHAN ,	02/2018	370.30 -	370.30	192.88	06/2018 -	-	-	1/4
1384	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000959]PWD,RAJASTHAN ,	02/2018	341.79 -	341.79	107.02	05/2018 -	-	-	1/4
1385	CONSTRUCTION OF 4 LANING BY CC PAVEMENT ON KOTA-DARAH OF NH-12 FROM 256/550 TO 289/550 UNDER EPC. - [N24000960]PWD,RAJASTHAN ,	12/2015	621.43 -	621.43	426.36	10/2016 -	-	-	3/4
1386	UP-GRADATION TO 2 LANE WITH PAVED SHOULDER FOR SECTION FROM KM 118.900 TO KM 156.955 BALOTRA TOSANDE - [N24000961]PWD,RAJASTHAN ,	01/2017	163.54 -	163.54	93.15	07/2017 -	-	-	2/4
1387	ALWAR-NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MORTH,RAJASTHAN ,	03/2019	178.13 -	178.13	5.90	- -	-	-	0/0
1388	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM ,	04/2013	151.59 240.58	151.59	196.76	08/2013 -	12/2019	76(O) -	0/0
1389	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM , ITEM RATE	04/2013	166.27 203.26	166.27	141.31	08/2013 -	-	-	0/0
1390	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM , ITEM RATE	01/2013	182.28 269.14	269.14	185.49	02/2013 09/2017	12/2019	82(O) 0	0/0
1391	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM , Central Sector Projects	04/2017	388.00 -	447.37	103.82	10/2017 -	-	-	2/4
1392	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA - [N24000766]NHIDCL,SIKKIM ,	04/2017	318.42 -	318.42	97.85	11/2017 -	-	-	2/4
1393	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM ,	03/2017	375.80 -	375.80	77.39	- -	-	-	0/0
1394	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM ,	11/2017	290.05 -	290.05	33.95	11/2017 -	-	-	1/4

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1395	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM ,	03/2018	264.84 -	264.84	.00	06/2018 -	-	-	0/4
1396	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU , PPP (BOT)	09/2011	1,250.00 -	1,250.00	1,333.68	12/2013 -	06/2020	78(O) -	0/0
1397	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU ,	06/2011	600.00 -	600.00	329.92	06/2013 01/2019	08/2020	86(O) 0	0/0
1398	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU , PPP (ANNUITY)	05/2010	374.00 -	374.00	237.00	05/2013 -	-	-	0/0
1399	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU , PPP (ANNUITY)	09/2011	485.00 -	485.00	406.68	08/2013 -	-	-	0/0
1400	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU , PPP (ANNUITY)	04/2012	624.00 -	624.00	350.79	04/2014 -	-	-	0/0
1401	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU , EPC	03/2015	258.97 -	268.92	.00	08/2015 -	-	-	0/0
1402	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU , EPC	03/2015	157.18 162.00	162.00	.00	07/2015 -	-	-	0/0
1403	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - - [N24000318]MORTH,TAMIL NADU , EPC	11/2015	154.14 -	154.14	.00	08/2015 -	-	-	0/0
1404	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU ,	05/2015	1,387.11 -	1,387.11	974.13	11/2017 -	07/2019	-	0/0
1405	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU ,	06/2015	563.92 -	563.92	93.53	12/2017 -	-	-	0/0
1406	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU ,	07/2014	401.11 -	401.11	273.89	01/2017 -	-	-	0/0
1407	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU , PPP (BOT)	03/2007	516.00 -	516.00	936.30	07/2008 -	-	-	0/0
1408	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU ,	02/2016	707.82 -	707.82	343.21	08/2018 -	03/2020	19(O) -	0/0
1409	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU ,	02/2016	641.17 -	641.17	354.03	07/2018 -	05/2020	22(O) -	0/0
1410	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU ,	03/2017	848.45 -	848.45	73.46	03/2020 -	03/2020	0(O) -	0/0
1411	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU , Central Sector Projects	03/2016	641.17 -	641.17	354.03	07/2016 -	05/2020	46(O) -	0/0
1412	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU , Central Sector Projects	08/2017	1,176.37 -	1,176.37	155.12	08/2017 -	09/2020	37(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1413	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU , Central Sector Projects	09/2017	244.27 -	244.27	141.45	09/2017 -	12/2019	27(O) -	0/0
1414	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU , Central Sector Projects	09/2017	1,227.87 -	1,227.87	225.96	09/2017 -	08/2020	35(O) -	0/0
1415	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU ,	12/2017	379.90 -	379.90	100.76	-	03/2020	-	0/0
1416	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU ,	02/2018	1,166.26 -	1,166.26	.00	-	02/2021	-	0/0
1417	FOUR LANING OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU , EPC	03/2018	505.35 -	505.35	36.14	-	11/2020	-	0/0
1418	FOUR LANING OF MADURAI- CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300) - [N24000827]NHAI,TAMIL NADU , EPC	03/2018	628.71 -	628.71	59.22	-	11/2020	-	0/0
1419	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU ,	03/2018	633.55 -	482.04	.00	-	-	-	0/0
1420	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU ,	03/2018	1,016.92 -	1,071.00	.00	-	04/2021	-	0/0
1421	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU ,	03/2018	2,065.96 -	2,169.00	.00	-	-	-	0/0
1422	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA , PPP (BOT)	04/2014	1,266.60 1,544.00	1,544.00	1,446.45	09/2016 -	09/2019	36(O) -	0/0
1423	REHABILITATION AND UPGRADEMENT OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]PWD,TELANGANA , EPC	01/2014	270.00 -	270.00	19.84	03/2016 -	-	-	1/4
1424	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA , EPC	03/2015	153.21 -	153.21	100.10	01/2017 -	09/2019	32(O) -	0/0
1425	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA ,	12/2015	1,423.96 897.03	897.03	737.19	11/2018 07/2019	12/2019	13(O) 0	0/0
1426	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA ,	03/2017	4,429.00 -	4,429.00	.00	03/2017 -	-	-	0/0
1427	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K - [N24000804]NHAI,TELANGANA ,	03/2018	802.65 -	802.65	80.29	-	-	-	0/0
1428	FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA ,	03/2018	950.63 -	950.63	62.00	-	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1429	FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA ,	03/2018	857.62 -	857.62	.03	-	-	-	0/0
1430	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHTRA - [N24000825]NHAI,TELANGANA ,	03/2018	828.29 -	828.29	.00	-	-	-	0/0
1431	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]PWD,TELANGANA ,	10/2016	298.32 -	298.32	77.44	02/2019 -	12/2019	10(O) -	0/0
1432	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]PWD,TELANGANA ,	10/2016	248.83 -	248.83	88.85	03/2019 -	12/2019	9(O) -	0/0
1433	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]PWD,TELANGANA ,	01/2017	244.54 -	244.54	137.63	05/2019 09/2019	-	-	0/0
1434	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON- THIRUMALAGIRI OF NH - [N24000983]PWD,TELANGANA ,	01/2017	196.52 -	196.52	103.12	10/2019 -	10/2019	0(O) -	0/0
1435	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA- KALWAKURTHY SECTI - [N24000984]PWD,TELANGANA ,	01/2017	283.00 -	283.00	152.35	12/2019 -	12/2019	0(O) -	0/0
1436	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA- RAVULAPALLY SECT - [N24000985]PWD,TELANGANA ,	01/2017	359.27 -	359.27	228.00	05/2019 -	08/2019	-	0/0
1437	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY- MALLEPALLY SECTION - [N24000986]PWD,TELANGANA ,	01/2017	300.00 -	300.00	99.46	05/2019 -	12/2019	7(O) -	0/0
1438	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH- SAMSHABAD SECTION) OF HYDERABAD- SAMSHABAD SECTION OF NH - [N24000987]PWD,TELANGANA ,	01/2018	283.15 -	283.15	42.22	05/2020 -	05/2020	0(O) -	0/0
1439	WIDENING AND STRENGTHENING OF EXISTING 2- LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]PWD,TELANGANA ,	01/2018	230.03 -	230.03	127.98	12/2019 -	12/2019	0(O) -	0/0
1440	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]PWD,TELANGANA ,	02/2018	206.13 -	206.13	127.86	06/2020 -	06/2020	0(O) -	0/0
1441	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]PWD,TELANGANA ,	02/2018	294.13 -	294.13	39.44	11/2019 -	11/2019	0(O) -	0/0
1442	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]PWD,TELANGANA ,	02/2018	220.28 -	220.28	37.58	11/2019 -	11/2019	0(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1443	REHABILITATION AND UPGRADE OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTING - [N24000992]PWD, TELANGANA ,	02/2018	426.52 -	426.52	225.51	04/2020 -	04/2020	0(O) -	0/0
1444	REHABILITATION AND UPGRADE OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]PWD, TELANGANA ,	03/2018	322.81 -	322.81	1.66	09/2020 -	09/2020	0(O) -	0/0
1445	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]PWD, TELANGANA ,	03/2018	626.76 -	626.76	80.66	07/2020 -	07/2020	0(O) -	0/0
1446	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]PWD, TELANGANA ,	01/2017	605.08 -	605.08	273.88	10/2019 -	10/2019	0(O) -	0/0
1447	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997]PWD, TELANGANA ,	03/2018	192.67 -	192.67	107.37	07/2019 -	12/2019	5(O) -	0/0
1448	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]PWD, TELANGANA ,	01/2019	193.19 -	193.19	.00	- -	-	-	0/0
1449	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL, TRIPURA , EPC	10/2014	369.00 -	369.00	308.97	03/2018 12/2019	12/2019	21(O) 0	3/4
1450	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]PWD, TRIPURA ,	10/2016	171.90 -	171.90	11.75	08/2020 -	08/2020	0(O) -	0/0
1451	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, UTTAR PRADESH , PPP (BOT)	02/2011	1,141.00 -	1,141.00	1,715.42	08/2013 -	-	-	0/0
1452	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI, UTTAR PRADESH , PPP (BOT)	03/2011	1,046.00 -	1,046.00	805.19	09/2013 -	-	-	0/0
1453	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH , PPP (BOT)	07/2012	291.36 -	291.36	459.07	01/2014 -	-	-	0/0
1454	ETAWAH CHAKERI - [N24000219]NHAI, UTTAR PRADESH , PPP (BOT)	03/2013	1,573.00 -	1,573.00	1,998.25	09/2015 -	-	-	0/0
1455	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH, UTTAR PRADESH , EPC	01/2014	282.41 -	282.41	155.53	03/2016 -	-	-	0/0
1456	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI, UTTAR PRADESH ,	05/2015	261.09 275.00	261.09	240.96	05/2017 -	-	-	0/0
1457	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI, UTTAR PRADESH ,	04/2014	351.34 -	351.34	433.68	01/2016 -	-	-	0/0
1458	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI, UTTAR PRADESH ,	09/2015	368.73 -	368.73	236.49	09/2016 03/2018	03/2018	-	0/0
1459	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI, UTTAR PRADESH ,	06/2014	301.04 -	301.04	207.94	01/2016 -	-	-	0/0
1460	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI, UTTAR PRADESH ,	04/2014	495.78 -	495.78	633.24	01/2016 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1461	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH , EPC	10/2013	445.89 -	653.29	464.05	03/2017 -	09/2019	30(O) -	0/0
1462	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]PWD,UTTAR PRADESH , ITEM RATE	11/2010	305.49 -	305.49	131.08	03/2017 -	-	-	0/0
1463	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH ,	09/2015	785.78 -	785.78	902.00	03/2018 -	-	-	0/0
1464	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH , PPP (BOT)	07/2015	1,657.20 -	1,657.20	2,345.00	01/2019 -	-	-	0/0
1465	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH ,	12/2015	611.65 -	611.65	728.24	06/2016 -	-	-	0/0
1466	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH ,	01/2016	815.28 2,182.03	815.28	520.89	06/2018 -	06/2020	24(O) -	0/0
1467	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH ,	01/2016	1,027.53 2,433.38	1,027.53	601.13	06/2018 -	06/2020	24(O) -	0/0
1468	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH ,	06/2016	667.00 2,257.49	667.00	464.05	07/2018 -	04/2020	21(O) -	0/0
1469	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH ,	12/2015	667.00 3,007.86	667.00	549.07	06/2018 -	04/2020	22(O) -	0/0
1470	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH , EPC	05/2013	164.54 -	164.54	89.14	08/2015 -	09/2019	49(O) -	0/0
1471	MEERUT-BULANDSHAHAH - [N24000539]NHAI,UTTAR PRADESH ,	01/2016	683.24 -	683.24	623.53	- -	-	-	0/0
1472	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH ,	01/2016	1,081.57 1,240.03	1,057.60	1,000.89	06/2019 12/2016	09/2019	3(O) 0	0/0
1473	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH ,	03/2016	676.73 -	676.73	632.21	04/2019 -	-	-	0/0
1474	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH ,	03/2016	1,404.50 -	1,404.50	92.37	- -	-	-	0/0
1475	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH ,	03/2016	1,396.74 -	1,396.74	227.26	- -	-	-	0/0
1476	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH ,	03/2016	1,587.49 -	2,982.00	276.87	04/2019 10/2019	10/2019	6(O) 0	0/0
1477	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH ,	03/2016	899.00 -	899.00	532.53	04/2019 07/2020	07/2020	15(O) 0	0/0
1478	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH ,	03/2016	1,668.00 -	1,668.00	946.08	- -	01/2020	-	0/0
1479	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH ,	03/2016	1,408.00 -	1,408.00	442.70	- -	07/2020	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1480	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH ,	03/2016	1,737.00 -	1,737.00	1,159.07	- -	04/2020	- -	0/0
1481	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH ,	08/2016	2,016.00 -	2,016.00	1,996.00	04/2019 11/2019	11/2019	7(O) 0	0/0
1482	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH ,	12/2016	534.55 -	531.00	433.62	- -	09/2019	- -	0/0
1483	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH ,	01/2017	450.68 -	450.68	397.62	- -	-	-	0/0
1484	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH ,	03/2017	1,373.28 -	1,373.28	571.96	03/2020 -	11/2020	8(O) -	0/4
1485	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH ,	03/2017	1,184.71 -	1,310.00	563.15	03/2020 -	08/2020	5(O) -	0/4
1486	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH ,	03/2017	1,989.00 2,602.09	1,989.00	852.57	03/2020 11/2017	05/2020	2(O) 0	0/0
1487	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH ,	03/2017	2,064.99 -	2,447.00	1,653.62	03/2020 -	03/2020	0(O) -	0/0
1488	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH ,	12/2017	1,232.21 3,207.63	1,087.00	473.11	- 02/2018	03/2020	- -2	0/0
1489	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH ,	12/2017	207.00 -	207.00	.00	- -	-	-	0/0
1490	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH ,	12/2017	305.00 -	305.00	.00	- -	-	-	0/0
1491	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH ,	01/2018	450.77 929.89	450.77	.00	- -	-	-	0/0
1492	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH ,	02/2018	670.50 -	670.50	.00	- -	-	-	0/0
1493	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH ,	03/2018	809.07 -	809.07	.00	- -	-	-	0/0
1494	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH ,	03/2018	925.40 -	925.40	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1495	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH ,	03/2018	1,117.84 1,684.93	1,117.84	.00	- 12/2018	12/2021	- 0	0/0
1496	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH ,	03/2018	2,140.93 -	2,140.93	.00	- -	-	-	0/0
1497	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH ,	03/2018	1,120.57 -	1,120.57	.00	- -	-	-	0/0
1498	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH ,	03/2018	1,025.80 -	677.07	115.83	- -	-	-	0/0
1499	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH ,	03/2018	1,115.28 -	770.04	216.33	- -	-	-	0/0
1500	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH ,	02/2018	972.77 1,444.25	972.77	.00	- 02/2019	02/2022	- 0	0/0
1501	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]PWD,UTTAR PRADESH ,	11/2016	326.99 327.00	326.99	.00	- -	-	-	0/0
1502	REHABILITATION AND UPGRADATION OF HARPALPUR -SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942]PWD,UTTAR PRADESH ,	03/2016	208.50 -	208.50	123.66	11/2019 -	11/2019	0(O) -	0/0
1503	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA - [N24001139]PWD,UTTAR PRADESH ,	10/2016	218.94 219.00	218.94	86.07	03/2020 -	03/2020	0(O) -	0/0
1504	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]PWD,UTTAR PRADESH ,	11/2016	215.16 215.00	215.16	157.79	09/2019 -	09/2019	0(O) -	0/0
1505	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]PWD,UTTAR PRADESH ,	03/2016	240.30 240.00	240.30	194.01	01/2020 -	01/2020	0(O) -	0/0
1506	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO - [N24001143]PWD,UTTAR PRADESH ,	10/2016	176.94 177.00	176.94	132.45	10/2018 -	09/2019	11(O) -	0/0
1507	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]MORTH,UTTAR PRADESH ,	10/2013	445.89 653.00	653.29	464.05	03/2017 -	09/2019	30(O) -	0/0
1508	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH - [N24001145]PWD,UTTAR PRADESH ,	05/2013	164.54 165.00	164.54	89.14	08/2015 -	09/2019	49(O) -	0/0
1509	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]PWD,UTTAR PRADESH ,	03/2016	249.50 -	249.50	150.70	05/2019 -	11/2019	6(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1510	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2- - [N24001147]PWD,UTTAR PRADESH ,	10/2016	239.63 -	239.63	211.57	02/2019 -	07/2019	-	0/0
1511	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148]PWD,UTTAR PRADESH ,	03/2016	599.34 -	599.34	449.19	01/2020 -	01/2020	0(O) -	0/0
1512	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - [N24001185]NHAI,UTTAR PRADESH , PPP BOT (Hybrid Annuity)	11/2017	2,159.00 -	2,159.00	715.78	01/2019 -	-	-	0/0
1513	REHABILITATION AND UPGRADATION OF BARAICH - SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA - [N24001202]PWD,UTTAR PRADESH ,	03/2016	388.83 -	388.83	280.17	12/2019 -	12/2019	0(O) -	0/0
1514	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203]PWD,UTTAR PRADESH ,	10/2016	218.90 -	218.90	23.37	03/2020 -	03/2020	0(O) -	0/0
1515	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]PWD,UTTAR PRADESH ,	07/2016	208.88 -	208.88	36.25	10/2019 -	10/2019	0(O) -	0/0
1516	R AND U FROM KM 385.00 TO KM 420.000 TO 2-LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404 - [N24001205]PWD,UTTAR PRADESH ,	12/2016	209.10 -	209.10	54.18	10/2019 -	10/2019	0(O) -	0/0
1517	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]PWD,UTTAR PRADESH ,	03/2018	263.89 -	263.89	67.69	04/2020 -	04/2020	0(O) -	0/0
1518	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]PWD,UTTAR PRADESH ,	03/2018	185.18 -	185.18	2.86	02/2020 -	02/2020	0(O) -	0/0
1519	FOUR LANING WIDENING & STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (JAN - [N24001208]PWD,UTTAR PRADESH ,	03/2018	288.30 -	288.30	.34	08/2020 -	08/2020	0(O) -	0/0
1520	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]PWD,UTTAR PRADESH ,	03/2016	296.50 -	296.50	.51	09/2020 -	09/2020	0(O) -	0/0
1521	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]PWD,UTTAR PRADESH ,	03/2018	306.59 -	306.59	.00	-	-	-	0/0
1522	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]PWD,UTTAR PRADESH ,	11/2018	281.45 -	281.45	.00	-	-	-	0/0
1523	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND ,	11/2011	478.51 -	478.00	315.11	10/2013 -	02/2020	76(O) -	0/0
1524	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND ,	03/2016	720.00 -	720.00	285.96	- 10/2020	10/2020	- 0	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1525	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND ,	03/2016	1,443.00 -	1,443.00	1,246.85	-	02/2020	-	0/0
1526	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND ,	11/2012	605.84 -	722.46	722.46	07/2018 12/2019	02/2020	19(O) 0	0/0
1527	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND ,	03/2018	274.31 -	274.31	19.22	05/2018 -	-	-	1/4
1528	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND ,	03/2018	403.36 -	403.36	89.19	06/2018 -	-	-	1/4
1529	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND ,	03/2018	417.24 -	417.24	87.71	05/2018 -	-	-	1/4
1530	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MORTH,UTTARAKHAND ,	12/2017	257.34 -	257.34	62.79	12/2019 -	12/2019	0(O) -	0/0
1531	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MORTH,UTTARAKHAND ,	12/2017	200.34 -	200.34	31.00	12/2019 -	12/2019	0(O) -	0/0
1532	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MORTH,UTTARAKHAND ,	12/2017	248.22 -	248.22	57.20	12/2019 -	12/2019	0(O) -	0/0
1533	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MORTH,UTTARAKHAND ,	06/2017	282.08 -	282.08	77.05	06/2019 -	12/2019	6(O) -	0/0
1534	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MORTH,UTTARAKHAND ,	11/2017	232.81 -	232.81	59.44	11/2019 -	11/2019	0(O) -	0/0
1535	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MORTH,UTTARAKHAND ,	11/2017	283.51 -	283.51	126.38	11/2019 -	11/2019	0(O) -	0/0
1536	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MORTH,UTTARAKHAND ,	11/2017	266.52 -	266.52	144.27	11/2019 -	11/2019	0(O) -	0/0
1537	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MORTH,UTTARAKHAND ,	02/2018	418.88 -	418.88	88.00	02/2020 -	02/2020	0(O) -	0/0
1538	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MORTH,UTTARAKHAND ,	02/2018	293.68 -	293.68	11.57	-	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1539	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MORTH,UTTARAKHAND ,	05/2018	248.00 -	248.00	.00	05/2020 -	05/2020	0(O) -	0/0
1540	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MORTH,UTTARAKHAND ,	03/2018	460.73 -	461.00	.00	- -	-	-	0/0
1541	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL,UTTARAKHAND ,	03/2018	1,383.78 -	1,383.78	107.45	07/2018 -	-	-	0/5
1542	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MORTH,UTTARAKHAND ,	08/2016	234.88 -	208.89	118.26	12/2017 -	12/2019	24(O) -	0/0
1543	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL , PPP (BOT)	02/2011	1,078.84 -	1,078.84	2,173.80	08/2013 -	12/2019	76(O) -	0/3
1544	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL , PPP (BOT)	02/2011	998.79 -	998.79	1,775.04	08/2013 -	06/2020	82(O) -	0/3
1545	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL , PPP (BOT)	04/2012	1,396.18 -	1,396.18	2,894.94	09/2014 -	12/2019	63(O) -	0/0
1546	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL , PPP (ANNUITY)	02/2012	702.16 -	702.16	733.33	07/2014 -	06/2020	71(O) -	0/0
1547	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH, WEST BENGAL ,	01/1991	322.00 -	322.00	56.41	03/2018 -	-	-	0/0
1548	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL ,	10/2015	361.15 -	361.15	144.71	- -	01/2020	-	0/0
1549	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL ,	12/2015	1,083.00 -	1,083.00	26.64	06/2018 -	12/2019	18(O) -	0/0
1550	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL , PPP (BOT)	04/2014	1,665.00 -	1,665.00	3,059.39	- -	-	-	0/0
1551	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK HALDIA - [N24000553]NHAI, WEST BENGAL ,	03/2016	229.37 -	229.37	78.31	11/2018 -	12/2019	13(O) -	0/0
1552	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL ,	09/2016	767.03 767.03	767.03	555.72	08/2018 -	09/2019	13(O) -	0/0
1553	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITA AND PANITNAKI I - [N24000770]NHIDCL, WEST BENGAL ,	03/2017	158.65 -	158.65	33.64	06/2018 -	-	-	0/0
1554	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI, WEST BENGAL ,	03/2018	1,261.98 -	1,261.98	.00	- -	-	-	0/0
1555	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B NH-31C NH-31 NH-10 O - [N24000871]PWD, WEST BENGAL ,	08/2014	600.87 720.97	720.97	644.60	11/2017 05/2019	05/2019	-	0/0
1556	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717 NH-31 NH-31C NH-317A O - [N24000873]PWD, WEST BENGAL ,	08/2014	823.20 937.76	937.76	737.80	11/2017 06/2019	06/2019	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1557	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]PWD,WEST BENGAL ,	03/2016	271.17 291.20	291.20	80.26	11/2018 11/2019	11/2019	12(O) 0	0/0
1558	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]PWD,WEST BENGAL ,	01/2017	396.86 396.86	396.86	179.65	09/2019 -	-	-	0/0
1559	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879]PWD,WEST BENGAL ,	03/2017	202.69 202.69	202.69	93.93	11/2019 -	11/2019	0(O) -	0/0
1560	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]PWD,WEST BENGAL ,	02/2018	426.18 426.18	426.18	219.94	09/2020 -	09/2020	0(O) -	0/0
1561	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]PWD,WEST BENGAL ,	02/2018	218.70 218.70	218.70	37.75	11/2020 -	11/2020	0(O) -	0/0
1562	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE BAGDO - [N24000883]PWD,WEST BENGAL ,	03/2018	254.30 254.30	254.30	52.85	10/2020 -	10/2020	0(O) -	0/0
1563	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]PWD,WEST BENGAL ,	03/2016	160.27 213.97	213.97	20.11	08/2019 -	08/2021	24(O) -	0/0
1564	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]PWD,WEST BENGAL ,	06/2016	236.78 263.26	263.26	59.92	08/2019 -	08/2021	24(O) -	0/0
1565	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]PWD,WEST BENGAL ,	04/2014	279.70 398.52	398.52	315.08	08/2017 07/2019	07/2019	-	0/0
	Total		5,09,942.21 -	5,31,171.55	2,67,315.79				247/963
	<u>SHIPPING AND PORTS</u>								
1566	JAL MARG VIKAS PROJECT - [N25000072]IWAI,MULTI STATE ,	01/2018	4,200.00 5,369.18	5,369.18	1,400.95	03/2023 03/2023	03/2023	0(O) 0	0/0
	Total		4,200.00 -	5,369.18	1,400.95				0/0
	<u>TELECOMMUNICATIONS</u>								
1567	GSM-RF EXPANSION PROJECT MTNL DELHI (3G) - [N26000105]MTNL,DELHI ,	06/2016	418.26 -	418.26	367.03	06/2017 -	-	-	0/0
1568	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]BSNL,MAHARASHTRA , Central Sector Projects	01/2018	231.80 240.10	240.10	117.63	10/2018 12/2019	12/2019	14(O) 3	0/0
1569	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE ,	03/2012	13,334.00 -	24,664.00	8,397.00	07/2015 -	05/2020	58(O) -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1570	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI,MULTI STATE , Central Sector Projects	09/2014	2,111.17 -	2,011.17	253.90	09/2014 -	-	-	0/70
	Total		16,095.23 -	27,333.53	9,135.56				0/70
	<u>URBAN DEVELOPMENT</u>								
1571	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH ,	07/2014	232.00 -	232.00	.00	- -	-	-	0/0
1572	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH ,	06/2014	157.84 -	169.16	163.98	03/2017 -	-	-	4/5
1573	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH ,	08/2007	246.90 -	246.90	.00	- -	-	-	0/0
1574	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP - [N28000108]CPWD,ANDHRA PRADESH ,	01/2018	206.58 -	206.58	82.23	03/2019 -	-	-	0/7
1575	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR ,	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72(O) -	0/0
1576	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR ,	02/2016	496.18 496.00	498.99	92.22	06/2017 -	10/2020	40(O) -	0/0
1577	DELHI MRTS PHASE-III - [N28000056]MMRC,DELHI ,	09/2011	38,585.00 -	38,585.00	34,763.00	03/2016 -	-	-	0/0
1578	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI ,	10/2013	1,219.21 -	2,000.00	374.71	10/2019 -	03/2021	17(O) -	0/7
1579	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI ,	07/2012	884.30 -	884.30	703.90	12/2015 -	-	-	0/0
1580	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI ,	06/2012	4,264.00 -	4,439.23	3,246.53	11/2019 -	11/2019	0(O) -	3/7
1581	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG NEW DELHI - [N28000087]CPWD,DELHI ,	06/2015	197.33 -	197.33	48.86	04/2019 -	11/2020	19(O) -	0/2
1582	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI ,	07/2016	2,694.00 -	2,694.00	.00	- -	-	-	0/0
1583	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS MINTO ROAD NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD,DELHI ,	11/2017	238.56 -	238.56	63.42	05/2020 -	05/2020	0(O) -	0/0
1584	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]CPWD,DELHI ,	12/2017	188.00 -	188.00	146.45	06/2019 -	-	-	0/0
1585	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI ,	10/2016	422.00 -	422.00	14.20	- -	12/2020	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1586	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI ,	10/2016	392.00 -	392.00	12.56	- 08/2020	03/2021	- 0	0/0
1587	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI ,	10/2016	248.20 -	248.20	33.39	04/2018 -	-	-	0/0
1588	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI ,	10/2017	271.90 -	271.90	33.56	11/2019 -	11/2019	0(O) -	0/0
1589	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI - [N28000123]CPWD,DELHI ,	07/2017	218.72 -	218.72	.00	- -	-	-	0/0
1590	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR GUJARAT - [N12000106]HSCL,GUJARAT ,	01/2013	175.00 -	175.00	1.83	- -	-	-	0/0
1591	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT ,	11/2014	10,773.00 -	10,773.00	6,057.03	12/2018 -	07/2020	19(O) -	0/0
1592	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH ,	11/2012	270.83 -	270.83	199.91	11/2014 -	10/2019	59(O) -	2/8
1593	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND ,	12/2007	253.92 253.92	253.92	193.97	06/2016 -	-	-	0/0
1594	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI KODERMA HAZARIBAG RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND ,	12/2007	200.00 -	200.00	131.15	03/2018 -	-	-	0/0
1595	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND ,	02/2014	787.29 -	787.29	285.30	12/2016 -	-	-	0/0
1596	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND ,	04/2013	170.00 -	170.00	88.91	04/2018 -	-	-	0/0
1597	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND ,	09/2012	171.86 -	171.86	85.33	03/2016 -	09/2020	54(O) -	1/6
1598	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA ,	05/2005	768.88 1,070.97	1,113.34	1,085.64	02/2014 -	-	-	0/0
1599	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA ,	07/2011	324.87 324.87	324.87	262.93	12/2015 -	-	-	0/0
1600	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA ,	02/2014	26,405.14 -	26,405.14	499.85	02/2019 -	03/2020	13(O) -	0/0
1601	RESIDENTIAL QUATERS FOR HAL BANGLORE - [N28000103]CPWD,KARNATAKA ,	12/2016	246.31 -	246.31	72.38	02/2020 -	09/2020	7(O) -	0/0
1602	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA ,	01/2010	165.23 -	165.23	92.05	10/2012 -	03/2020	89(O) -	1/7
1603	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA ,	07/2012	5,181.79 -	5,687.79	5,188.00	07/2017 -	12/2019	29(O) -	0/0
1604	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST - [N28000112]CPWD,KERALA ,	09/2017	150.29 -	150.29	2.58	03/2020 -	03/2020	0(O) -	2/7

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1605	BHOPAL METRO RAIL - [N28000124]MPMRCL,MADHYA PRADESH ,	11/2018	6,941.40 -	6,941.40	34.12	02/2023 -	02/2023	0(O) -	0/0
1606	INDORE METRO RAIL - [N28000125]MPMRCL,MADHYA PRADESH ,	11/2018	7,500.80 -	7,500.80	42.62	02/2023 -	02/2023	0(O) -	0/0
1607	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD,MAHARASHTRA ,	06/2010	205.00 -	205.00	165.47	03/2012 -	-	-	18/20
1608	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA ,	08/2014	8,680.00 -	8,680.00	6,237.34	03/2018 -	12/2019	21(O) -	0/0
1609	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA ,	07/2013	23,136.00 -	23,136.00	.00	01/2015 -	05/2020	64(O) -	0/0
1610	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY POWAI MUMBAI - [N28000117]CPWD,MAHARASHTRA ,	01/2018	223.37 -	223.37	33.01	07/2020 09/2020	09/2020	2(O) 0	3/14
1611	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA ,	12/2016	11,420.00 -	11,420.00	2,896.26	11/2021 01/2022	01/2022	2(O) 0	0/0
1612	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR , Central Sector Projects	02/2014	216.69 -	216.69	52.00	03/2015 -	10/2020	67(O) -	0/10
1613	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA ,	04/2014	151.33 -	151.33	7.15	09/2017 -	-	-	0/0
1614	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD,ODISHA ,	01/2019	790.79 -	800.00	2.56	03/2022 -	03/2022	0(O) -	0/0
1615	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR PUNJAB - [N28000088]CPWD,PUNJAB ,	02/2014	388.00 -	488.28	437.01	05/2017 -	10/2019	29(O) -	8/12
1616	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR PUNJAB - [N28000102]CPWD,PUNJAB ,	08/2016	294.00 -	294.00	203.32	04/2019 -	02/2020	10(O) -	6/8
1617	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR PUNJAB - [N28000120]CPWD,PUNJAB ,	01/2018	430.00 -	430.00	77.69	05/2020 -	01/2021	8(O) -	1/5
1618	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN ,	05/2015	189.00 -	189.00	.00	03/2017 -	-	-	0/0
1619	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN ,	12/2016	549.31 559.47	559.47	348.69	07/2019 12/2019	02/2020	7(O) 0	0/0
1620	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU ,	02/2009	14,600.00 -	19,058.00	16,352.87	12/2015 -	-	-	12/24
1621	C/O OF 152 NOS TYPE-II 304 NOS TYPE-III 76 NOS TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD,TAMIL NADU ,	12/2015	209.00 -	209.00	130.62	10/2019 -	03/2020	5(O) -	1/6
1622	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU ,	06/2016	3,770.00 -	3,770.00	.00	03/2018 -	-	-	0/19
1623	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU ,	11/2017	348.77 -	348.77	14.52	- -	11/2021	- -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(September 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1624	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA ,	10/2016	209.84 -	209.84	35.79	03/2020 -	05/2021	14(O) -	0/5
1625	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA ,	03/2007	149.73 173.00	175.94	178.65	12/2015 -	-	-	0/0
1626	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA ,	12/2007	202.61 227.00	227.00	199.95	12/2016 -	-	-	0/0
1627	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA ,	10/2011	175.49 206.71	206.71	141.28	12/2016 -	-	-	0/0
1628	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH ,	01/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 -	-	-	0/0
1629	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH ,	11/2017	171.72 -	171.72	32.00	03/2020 -	03/2020	0(O) -	0/0
1630	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND ,	12/2008	114.26 266.00	266.00	.00	12/2013 -	10/2019	70(O) -	0/0
1631	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL , Central Sector Projects	08/2012	185.37 -	185.37	178.30	03/2016 -	-	-	0/0
1632	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL ,	02/2014	156.57 -	156.57	156.13	08/2016 -	10/2019	38(O) -	10/16
1633	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL , Central Sector Projects	10/2014	162.88 -	162.88	138.89	04/2018 -	-	-	5/6
	Total		1,86,663.06 -	1,93,294.88	85,310.09				77/201
	<u>WATER RESOURCES</u>								
1634	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA,ANDHRA PRADESH , National Project	02/2009	10,151.04 -	55,548.87	16,417.99	03/2020 -	06/2021	15(O) -	0/19
1635	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPPB,MAHARASHTRA ,	03/2017	233.57 -	233.57	32.20	12/2019 -	12/2019	0(O) -	0/0
	Total		10,384.61 -	55,782.44	16,450.19				0/19
	Grand Total		19,47,462.67	23,41,784.84	9,96,613.94				2774/5440

Annexure

Annexure - I

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE (SEPTEMBER 2019)

(All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	A & N ISLANDS	9	2,786.01	2,893.59	445.12
2	ANDHRA PRADESH	74	1,19,083.46	1,68,703.11	47,161.36
3	ARUNACHAL PRADESH	40	21,795.08	40,754.39	21,939.38
4	ASSAM	48	26,216.03	31,003.54	14,762.42
5	BIHAR	94	90,608.62	1,27,798.63	62,907.83
6	CHHATISGARH	34	73,625.1	85,279.62	43,653.26
7	D & N HAVELI	1	6,086.08	5,842.31	4,784.88
8	DELHI	25	55,985.34	63,868.57	41,784.89
9	GOA	10	5,325.87	5,336.3	1,812.94
10	GUJARAT	56	64,665.47	71,921.79	47,175.99
11	HARYANA	40	30,880.96	33,054.71	15,054.41
12	HIMACHAL PRADESH	13	18,053.17	28,163.7	12,407.23
13	JAMMU AND KASHMIR	13	20,822.23	46,498.48	34,430.06
14	JHARKHAND	47	62,036.07	67,344.06	26,929.59
15	KARNATAKA	63	73,084.28	76,598.88	20,826.44
16	KERALA	20	36,309.6	39,755.52	14,186.92
17	MADHYA PRADESH	78	86,555.71	93,301.25	43,303.29
18	MAHARASHTRA	258	2,36,169.1	2,46,235.56	98,553.38
19	MANIPUR	5	6,002.36	14,012.39	9,404.35
20	MEGHALAYA	6	2,760.77	7,854.31	1,217.04
21	MIZORAM	13	7,757.62	11,189.69	4,763.58
22	MULTI STATE	130	3,17,331.17	4,24,714.5	1,39,175.98
23	NAGALAND	26	14,842.43	17,115.91	1,908.33
24	ODISHA	92	1,06,784.06	1,09,220.71	44,064.56
25	PUNJAB	27	13,539.35	15,038.78	9,195.74
26	RAJASTHAN	63	47,345.31	54,833.78	34,475.01
27	SIKKIM	9	3,476.73	6,368.17	1,122.03
28	TAMIL NADU	65	1,16,109.47	1,34,527.19	65,660.6
29	TELANGANA	56	39,959.69	42,435.36	13,611.66
30	TRIPURA	7	1,977.29	2,139.55	1,099.34
31	UTTAR PRADESH	118	1,44,722.96	1,49,516	66,300.7
32	UTTARAKHAND	31	35,661.33	44,552.75	15,105.34
33	WEST BENGAL	64	59,103.95	73,911.74	37,390.29
TOTAL		1,635	19,47,462.67	23,41,784.84	9,96,613.94

List of Projects in which Expenditure is More than Approved Cost

Annexure - II

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	9/2003	3,492.00 -	6,840.00	5,821.38	09/2010 -	10/2021
	Total		3,492.00 -	6,840.00	5,821.38		
	<u>COAL</u>						
	<u>Mahanadi Coal Fields Limited</u>						
2	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]	12/2007	457.77 -	457.77	539.59	03/2013 -	03/2022
3	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.10 -	490.10	501.82	03/2017 -	03/2020
4	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]	12/2007	172.08 -	172.08	347.15	03/2010 -	03/2022
5	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]	8/2008	207.28 -	207.28	228.90	03/2012 -	03/2021
	<u>Singareni Colliers Company Limited</u>						
6	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	286.19	03/2012 -	03/2024
	<u>South-Eastern Coal Fields Limited</u>						
7	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	9/2008	152.43 -	459.49	193.40	03/2015 -	03/2020
	Total		1,728.69 -	2,235.58	2,097.05		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation Ltd</u>						
8	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	9/2014	505.58 -	523.00	508.29	03/2018 -	-
	Total		505.58 -	523.00	508.29		
	<u>PETROLEUM</u>						
	<u>Indian Strategic Petroleum Reserves Ltd</u>						
9	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	1/2006	993.00 -	1,693.00	1,549.85	01/2012 -	-
	<u>Oil & Natural Gas Corporation Limited</u>						
10	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	3/2011	861.79 -	1,683.06	1,322.31	05/2013 12/2019	12/2019
	Total		1,854.79 -	3,376.06	2,872.16		

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>POWER</u>						
	<u>National Hydro-Electric Power Corporation</u>						
11	PARBATI HEP (4X200 MW) (NHPC) II - [N180100210]	9/2002	3,919.59 -	9,997.11	7,642.51	09/2009 -	12/2021
12	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [N180100221]	9/2003	6,285.33 -	19,496.34	10,989.45	09/2010 -	-
	<u>National Thermal Power Corporation</u>						
13	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	12,865.92	12,188.01	01/2018 03/2020	03/2020
14	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]	4/2012	9,750.89 -	12,176.28	9,794.00	02/2017 06/2020	06/2020
15	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	1/2007	5,353.00 -	9,996.59	7,918.78	07/2012 -	09/2020
16	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	12,457.15	10/2017 03/2020	03/2020
	<u>Power Grid Corporation Of India Limited</u>						
17	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	2/2009	11,130.19 -	14,719.10	12,814.08	08/2013 -	03/2022
18	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	564.32	06/2014 -	10/2019
19	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [N180100258]	5/2005	1,779.29 -	2,187.32	2,237.45	11/2008 -	-
	<u>Thdc India Limited</u>						
20	DHUKWAN SMALL HYDRO PROJECT - [N18000189]	5/2011	195.42 -	294.60	310.08	02/2014 -	12/2019
21	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	7/2006	1,657.00 -	5,024.35	3,047.08	02/2016 -	06/2022
	Total		64,042.75 -	1,00,136.89	79,962.91		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
22	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	4/2011	184.06 -	305.00	269.39	03/2019 12/2019	12/2019
23	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [N220100181]	2/1997	2,271.50 -	3,712.50	2,380.30	03/2021 -	03/2022
	<u>East Central Railways</u>						
24	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [N220100222]	3/1999	1,033.07 -	3,376.00	3,307.82	- -	03/2021
25	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	4/2013	213.01 -	425.17	406.05	- -	01/2020
26	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIIYAWAN-BIHARSHARIF, - [N22000476]	4/1991	329.39 -	1,483.14	1,029.84	- -	12/2021
27	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [N220100240]	4/1997	324.73 -	1,050.00	1,040.00	03/2012 -	03/2020
	<u>East Coast Railway</u>						

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
28	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319 <u>Eastern Railways</u>	3/2012	155.81 -	238.03	226.50	03/2020 -	03/2021
29	DEOGHAR - SULTANGANJ (INL), ER - [220100273	4/2000	607.09 -	1,425.44	637.42	02/2013 -	03/2024
30	PIRPAINTI-BHAGALPUR - [N22000222	4/2011	261.38 -	471.81	467.50	- -	05/2019
31	BANDEL-BOINCHI 3RD LINE - [N22000221	4/2011	288.35 -	382.90	382.90	- -	03/2020
32	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238	4/2011	175.80 -	245.41	245.41	- -	03/2021
33	MONIGRAM- NIMTITA - [N22000301	4/2012	250.93 -	310.70	263.08	- -	03/2024
	<u>Metropolitan Rapid Transport Projects</u>						
34	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	3/2000	1,049.69 -	3,404.92	3,837.57	12/2006 -	-
35	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135	3/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021
	<u>North Central Railway</u>						
36	ETAWAH-MAINPURI (NL),NCR - [220100318	4/1997	120.00 -	346.00	345.51	12/2008 -	-
	<u>North East Frontier Railway</u>						
37	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207	4/2010	241.52 -	394.28	272.88	- -	03/2021
38	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209	4/1999	819.23 -	1,871.00	1,082.01	- -	-
39	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHOWA-JAIN - [N22000499	2/1999	380.60 -	1,871.00	1,087.60	04/2010 -	-
	<u>North Eastern Railway</u>						
40	HATHUA-BHATNI (N L) (NER) - [220100319	4/2005	230.03 -	230.03	277.14	12/2022 -	12/2022
41	CHHAPRA-BALLIA UP - [N22000134	3/2013	295.00 -	477.31	328.19	01/2019 -	01/2020
	<u>North Western Railway</u>						
42	AJMER-BANGURGRAM - [N22000155	4/2011	213.39 -	303.56	262.32	11/2019 -	05/2020
43	ALWAR-BANDIKUI DOUBLING - [N22000157	4/2013	242.09 -	410.00	351.23	02/2019 -	05/2020
	<u>Northern Railway</u>						
44	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274	4/2007	336.91 -	800.00	512.67	- -	03/2022
45	NANGALDAM-TALWARA(NL),NR - [220100188	3/1981	450.00 -	2,010.00	654.07	07/2012 -	03/2024
46	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492	3/2002	625.00 -	845.58	834.59	03/2016 -	03/2021

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
47	HARIDWAR-LAKSAR - [N22000289 <u>Rail Vikas Nigam Ltd.</u>	4/2012	219.83 -	346.63	229.48	- -	06/2020
48	HARIDASPUR-PARADEEP(NL) - [220100285	4/1996	1,185.64 -	1,844.47	1,783.59	12/2017 -	03/2020
49	BANASPANI- JAKHPURA - DOUBLING - [N22000412	3/2009	942.95 -	1,120.00	1,010.21	03/2019 -	06/2022
50	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410	3/2006	948.04 -	1,500.00	1,323.18	03/2020 -	03/2021
51	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407	3/2009	713.48 -	1,950.00	1,957.22	03/2020 -	03/2020
52	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404	4/2011	927.01 -	1,200.00	1,147.34	03/2019 -	03/2020
53	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213	4/2012	632.68 -	816.55	686.11	03/2016 -	12/2020
54	AHMEDABAD-BOTAD (GC) - [N22000140	4/2012	975.62 -	1,082.32	994.30	12/2021 -	12/2021
55	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313	3/2012	1,503.71 -	1,503.71	1,563.45	03/2020 -	03/2022
56	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	4/2000	133.41 207.00	385.00	386.30	03/2009 03/2009	12/2019
	<u>South Central Railway</u>						
57	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192	3/1996	164.36 -	1,050.00	999.64	02/2009 -	-
	<u>South East Central Railway</u>						
58	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	4/2005	383.79 -	1,413.76	1,324.64	- -	10/2019
	<u>South Eastern Railway</u>						
59	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	4/2012	148.77 -	377.00	180.95	12/2016 08/2018	12/2019
	<u>Southern Railway</u>						
60	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079	9/2007	724.69 -	2,072.50	1,386.59	02/2019 -	02/2020
61	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187	4/1999	198.68 -	556.64	303.72	- -	-
62	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444	2/1999	257.00 257.00	257.00	268.31	03/2018 -	-
63	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441	2/1996	268.87 -	950.00	927.86	03/2005 -	-
64	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215	4/2011	120.70 -	1,800.00	170.47	03/2019 -	12/2019
65	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	9/1995	303.98 -	980.00	669.21	03/2020 -	03/2021
	<u>West Central Railway</u>						
66	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314	4/2001	424.60 -	2,909.99	1,926.25	03/2021 -	03/2023

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
67	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232 <u>Western Railway</u>	9/1998	247.66 -	6,093.31	1,835.18	05/2008 -	03/2023
68	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125	4/2006	117.36 196.95	202.35	809.40	03/2011 03/2017	03/2017
69	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121	4/2008	829.74 -	1,310.23	1,394.73	03/2020 03/2021	03/2021
	Total		28,345.73 -	66,686.21	49,672.84		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Dept Of Road Transport & Highways</u>						
70	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259	3/2015	280.16 -	290.59	280.47	- -	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
71	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325	10/2015	179.82 -	179.82	197.77	01/2019 -	-
	<u>National Highways Authority Of India</u>						
72	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 -	525.00	488.37	02/2009 07/2019	07/2019
73	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515	4/2014	1,665.00 -	1,665.00	3,059.39	- -	-
74	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509	4/2010	1,170.52 -	1,170.52	2,051.36	06/2012 -	-
75	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508	7/2015	1,871.34 -	1,871.34	3,495.79	01/2018 12/2018	12/2019
76	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494	5/2013	1,055.00 -	1,601.77	1,393.40	11/2015 -	-
77	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477	2/2008	1,673.70 -	1,673.70	3,326.93	10/2011 -	-
78	NAGPUR - KONDHALI - [N24000472	9/2005	168.00 -	168.00	226.24	06/2006 -	-
79	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462	5/2014	1,655.01 -	1,655.01	1,867.51	08/2016 -	12/2020
80	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460	12/2015	611.65 -	611.65	728.24	06/2016 -	-
81	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453	1/2015	972.50 -	972.50	1,492.00	07/2017 -	10/2019
82	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	3/2017	988.34 -	1,043.28	1,094.73	03/2020 -	08/2020
83	4 LANING OF KSHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638	11/2012	605.84 -	722.46	722.46	07/2018 12/2019	02/2020
84	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624	9/2016	1,244.10 -	1,244.10	1,335.00	- -	02/2020

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
85	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622	9/2016	950.69 -	1,108.00	1,354.09	08/2019 -	12/2020
86	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621	9/2016	1,239.82 -	1,239.82	1,280.27	- -	05/2020
87	TRICHY - KARUR - [N24000528	3/2007	516.00 -	516.00	936.30	07/2008 -	-
88	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517	12/2015	479.20 -	479.20	711.38	05/2018 03/2018	10/2019
89	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452	7/2015	1,657.20 -	1,657.20	2,345.00	01/2019 -	-
90	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450	9/2015	785.78 -	785.78	902.00	03/2018 -	-
91	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445	8/2014	822.90 -	822.90	844.08	04/2018 -	-
92	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432	9/2015	414.51 -	414.00	531.36	05/2018 03/2019	05/2020
93	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER- FATEHPUR-SALA - [N24000426	11/2012	530.07 -	530.07	556.02	08/2016 -	12/2019
94	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367	4/2014	495.78 -	495.78	633.24	01/2016 -	-
95	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360	4/2014	351.34 -	351.34	433.68	01/2016 -	-
96	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206	4/2012	1,396.18 -	1,396.18	2,894.94	09/2014 -	12/2019
97	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205	12/2011	1,047.00 -	1,047.00	1,874.43	06/2014 -	03/2019
98	4-LANING OF BRAHAMPORE-FARAKA - [N24000203	2/2011	998.79 -	998.79	1,775.04	08/2013 -	06/2020
99	4-LANING OF FARAKA-RAIGANJ - [N24000202	2/2011	1,078.84 -	1,078.84	2,173.80	08/2013 -	12/2019
100	MUZAFFARNAGAR-HARIDWAR - [N24000201	9/2011	754.00 -	754.00	1,364.18	03/2013 -	12/2019
101	PANIKHOLI-RIMOLI - [N24000197	3/2012	1,410.00 -	1,410.00	1,935.14	09/2014 -	-
102	SRINAGAR TO BANIHAL - [N24000189	6/2011	1,100.70 -	1,100.70	2,880.38	06/2014 09/2017	09/2020
103	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188	5/2011	511.54 -	511.54	566.60	11/2013 -	-
104	4-LANNING OF CHAPRA-HAJIPUR - [N24000187	1/2011	575.00 -	575.00	843.67	07/2013 -	-
105	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224	10/2012	1,928.22 -	2,945.00	3,070.11	04/2015 -	-
106	AHMEDABAD TO VADODARA SECTION - [N24000222	1/2013	2,125.24 -	2,521.24	4,659.71	12/2015 -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
107	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	1,998.25	09/2015 -	-
108	KRISHNANAGAR-BERHAMPUR - [N24000209]	2/2012	702.16 -	702.16	733.33	07/2014 -	06/2020
109	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]	7/2012	291.36 -	291.36	459.07	01/2014 -	-
110	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]	10/2011	375.09 -	375.09	494.33	04/2014 -	-
111	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]	9/2011	574.00 -	574.00	768.73	03/2014 -	-
112	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]	11/2011	1,535.00 -	1,535.00	3,220.15	05/2014 -	10/2019
113	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]	4/2011	571.00 -	571.00	582.53	10/2013 -	-
114	KANDLA - MUNDRA PORT - [N24000175]	1/2011	953.88 -	953.88	976.79	07/2013 -	-
115	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]	9/2011	1,250.00 -	1,250.00	1,333.68	12/2013 -	06/2020
116	GHAZIABAD-ALIGARH NH-91 - [N24000170]	2/2011	1,141.00 -	1,141.00	1,715.42	08/2013 -	-
117	INDORE-JHABUA-GUJRAT/MP - [N24000136]	10/2010	1,175.00 -	1,175.00	1,342.77	04/2013 -	-
118	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]	11/2013	1,916.79 -	1,916.79	1,948.92	11/2016 -	-
119	NALBARI TO BIJNI (AS-6) - [N24000047]	12/2003	225.00 -	225.00	328.47	06/2008 -	10/2019
120	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 -	230.00	337.76	04/2008 -	03/2020
121	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61 -	360.84	451.15	04/2010 -	07/2019
122	INDORE-DEWAS(NH-3) - [N24000159]	11/2010	325.00 -	325.00	469.54	05/2013 -	-
123	PUNE-SATARA(NH-4) - [N24000156]	10/2010	1,724.55 -	1,724.55	2,387.46	03/2013 -	12/2019
124	4 LANING OF NAGPUR-BETUL - [N24000155]	2/2011	2,498.76 -	2,498.76	2,531.46	08/2014 -	-
125	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]	2/2010	617.00 -	617.00	943.17	08/2012 -	12/2019
126	PATNA-MUZZAFFARPUR - [N24000165]	8/2010	671.30 -	671.30	885.47	02/2013 -	-
127	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]	7/2010	1,813.76 -	1,813.76	2,393.99	07/2013 -	-
128	NASHRI- CHANANI - [N24000162]	5/2011	2,159.00 -	2,519.00	4,705.68	06/2015 -	-
129	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]	7/2010	1,987.00 -	1,987.00	2,700.65	07/2015 12/2019	09/2020
130	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]	12/2003	160.00 -	167.98	223.81	05/2008 -	06/2019

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
131	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]	5/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	-
132	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	5/2009	1,108.00 -	2,967.50	3,986.72	11/2011 -	03/2020
	<u>National Highways Development Project</u>						
133	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]	10/2013	445.89 -	653.29	464.05	03/2017 -	09/2019
134	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]	11/2013	497.05 -	881.05	544.84	05/2017 -	05/2020
	<u>Public Works Dept Of State</u>						
135	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]	11/2010	624.41 -	992.67	853.82	03/2011 -	12/2019
136	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]	8/2010	193.69 -	327.92	254.24	10/2010 -	12/2019
137	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]	8/2010	186.96 -	305.61	275.06	09/2014 -	12/2019
138	CITTORGARH-NEEMACH (4L) OF NH-79 AND NIMBAHARA PRATAPGARH (2L+PS) OF NH-113 UNDER PPP. - [N24000955]	10/2012	511.21 -	511.21	814.79	10/2013 -	-
139	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]	12/2011	159.39 -	159.39	210.29	11/2017 -	09/2019
140	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]	9/2012	511.00 -	511.00	2,323.04	10/2013 -	-
141	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]	8/2010	195.04 -	377.99	305.38	10/2010 -	06/2020
142	4-LANING OF LAMBRA-SHAKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]	11/2015	847.02 -	847.02	1,086.49	- 09/2019	-
	Total		66,882.90 -	73,214.44	1,03,169.28		
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
143	NMDC INTEGRATED STEEL PLANT - [N12000086]	1/2010	15,525.00 -	23,140.00	16,064.29	05/2015 07/2020	07/2020
	Total		15,525.00 -	23,140.00	16,064.29		
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
144	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]	2/2014	388.00 -	488.28	437.01	05/2017 -	10/2019

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
145	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076] <u>Chennai Metro Rail Ltd</u>	6/2014	157.84 -	169.16	163.98	03/2017 -	-
146	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084] <u>Hindustan Steelwork Construction Limited</u>	2/2009	14,600.00 -	19,058.00	16,352.87	12/2015 -	-
147	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]	5/2005	768.88 1,070.97	1,113.34	1,085.64	02/2014 -	-
148	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098] <u>Kochi Metro Rail Corporation Ltd</u>	3/2007	149.73 173.00	175.94	178.65	12/2015 -	-
149	KOCHI METRO RAIL PROJECT - [N28000081]	7/2012	5,181.79 -	5,687.79	5,188.00	07/2017 -	12/2019
	Total		21,246.24 -	26,692.51	23,406.15		
	<u>WATER RESOURCES</u>						
	<u>Polavaram Project Authority</u>						
150	POLAVARAM IRRIGATION PROJECT - [N30000002]	2/2009	10,151.04 -	55,548.87	16,417.99	03/2020 -	06/2021
	Total		10,151.04 -	55,548.87	16,417.99		
	Grand Total		2,13,774.72	3,58,393.56	2,99,992.34		

Details of Projects Ahead of Schedule w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
	<u>South-Eastern Coal Fields Limited</u>						
1	BATURA OCP (2.0 MTY) - [N06000049]	8/2015	1,186.64 -	203.82	121.39	03/2023 -	03/2021
	Total		1,186.64 -	203.82	121.39		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
2	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY [N16000260]	2/2016	554.00 -	554.00	363.86	02/2020 -	10/2019
	<u>Indian Oil Corporation Limited</u>						
3	PARADIP HYDERABAD PIPELINE - [N16000194]	1/2015	2,321.00 3,338.00	3,338.00	1,820.56	12/2020 -	08/2020
4	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]	9/2015	324.00 -	324.00	154.50	06/2020 -	03/2020
5	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]	5/2016	664.00 -	664.00	601.75	12/2020 -	02/2020
6	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]	8/2017	315.00 -	315.00	112.13	12/2021 -	12/2020
7	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]	3/2018	3,712.00 -	3,696.00	309.62	09/2022 -	06/2021
8	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]	8/2017	384.58 -	384.58	85.86	04/2021 -	04/2020
	Total		8,274.58 -	9,275.58	3,448.28		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
9	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	1/2013	12,964.60 17,304.00	17,304.00	13,970.00	05/2018 12/2021	03/2021
	Total		12,964.60 -	17,304.00	13,970.00		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
10	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	2/2015	3,627.47 -	3,627.47	686.42	03/2024 -	03/2022
	<u>East Central Railways</u>						
11	GARHWA ROAD-RAMNA - [N22000465]	3/2015	348.23 -	348.23	177.12	03/2021 -	12/2020
	<u>North East Frontier Railway</u>						

Costing Rs. 150 Crore and above

(September 2019)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
12	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	4/2015	2,232.32 -	2,182.00	654.38	03/2022 -	03/2020
13	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	4/2016	602.27 -	612.00	257.73	12/2021 -	03/2020
	<u>North Eastern Railway</u>						
14	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,295.42 -	1,295.42	328.56	03/2022 -	12/2019
	<u>Rail Vikas Nigam Ltd.</u>						
15	BHANUPALI-BILASPUR BERI NL - [N22000273]	4/2008	2,966.99 -	7,000.00	398.76	12/2026 -	12/2025
16	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78 -	723.78	.19	12/2025 -	03/2025
	Total		11,796.48 -	15,788.90	2,503.16		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways</u>						
17	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]	2/2017	429.43 -	429.43	203.52	11/2017 03/2020	11/2019
18	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969]	1/2017	263.45 -	263.45	57.97	09/2017 03/2020	09/2019
19	PARSHURAM GHAT TO ARAWALI - [N24001133]	4/2016	983.14 983.14	983.14	655.15	12/2019 -	11/2019
20	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]	1/2017	576.48 -	576.48	207.93	01/2018 03/2020	01/2020
	<u>National Highways Authority Of India</u>						
21	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]	10/2015	447.29 746.43	746.43	600.33	12/2017 06/2020	12/2019
22	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]	8/2016	1,388.34 2,525.80	2,525.80	1,449.00	09/2019 03/2020	09/2019
23	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]	3/2017	247.02	157.49	21.89	03/2020 02/2021	02/2020
24	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]	3/2017	296.19 -	254.00	248.60	03/2020 -	09/2019
25	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]	3/2017	639.79	552.90	491.93	03/2020 -	09/2019
26	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]	3/2017	648.32 -	503.10	497.15	03/2020 -	11/2019
27	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]	3/2017	165.50	172.16	117.09	03/2020 -	09/2019
28	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]	4/2017	894.00 -	894.00	730.00	04/2020 -	11/2019
	<u>Public Works Dept Of State</u>						
29	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]	1/2017	247.25 -	247.25	144.71	03/2019 03/2020	09/2019

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		7,226.20	8,305.63	5,425.27		
	Grand Total		41,448.50	50,877.93	25,468.10		

Details of On Schedule Projects w.r.t. Original Schedule

Annexure - IV

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]	12/2016	859.86 -	860.00	232.44	03/2021 -	03/2021
2	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN - [N04000085]	7/2018	353.27 -	353.27	114.29	09/2020 -	09/2020
3	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]	8/2018	951.28 -	951.28	71.55	10/2021 -	10/2021
4	CONSTRUCTION OF NEW DOMESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082]	5/2018	539.20 -	539.20	25.64	10/2022 -	10/2022
5	CONSTRUCTION OF TERMINAL BUILDING & ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	7/2018	323.19 -	323.19	10.14	09/2021 -	09/2021
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICATION - [N04000079]	3/2017	358.89 -	358.89	29.73	04/2021 -	04/2021
7	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]	6/2018	1,383.00 -	1,383.00	210.62	09/2021 -	09/2021
8	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA - [N04000081]	1/2019	264.99 -	264.99	0.42	11/2021 -	11/2021
	Total		5,033.68 -	5,033.82	694.83		
	<u>COAL</u>						
	<u>Bharat Coking Coal Limited</u>						
9	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	5.24	03/2021 -	03/2021
	<u>Central Coal Fields Limited</u>						
10	NORTH URIMARI EXPANSION OCP - [N06000182]	3/2019	1,553.06 -	1,553.06	163.23	03/2023 -	03/2023
11	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	194.12	03/2020 -	03/2020
	<u>Eastern Coal Fields Limited</u>						
12	TILABONI UG MINE - [N06000172]	2/2019	916.62 -	916.62	-	03/2027 -	03/2027
13	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	315.69	03/2022 -	03/2022
14	NAKRAKONDA KUMARDIH B OCP - [N06000170]	8/2018	502.68 -	502.68	-	03/2029 -	03/2029
15	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	83.23	03/2022 -	03/2022
16	CHITRA EAST (RCE) OCP - [N06000169]	8/2018	513.98 -	513.98	90.23	03/2024 -	03/2024

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
17	SIDULI MINE (OC AND UG) - [N06000165]	5/2018	535.18 -	535.18	-	03/2026 -	03/2026
	<u>Mahanadi Coal Fields Limited</u>						
18	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	440.13	03/2021 -	03/2021
19	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]	11/2018	2,838.87 -	2,838.87	1,113.66	03/2029 -	03/2029
20	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	1,549.76	03/2026 -	03/2026
21	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]	5/2018	2,434.75 -	2,434.75	83.20	03/2027 -	03/2027
	<u>Neyveli Lignite Corporation</u>						
22	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	7,532.67	11/2021 -	11/2021
	<u>Northern Coal Fields Limited</u>						
23	SEMARIA OPENCAST PROJECT - [N06000176]	5/2019	396.58 -	396.58	-	03/2026 -	03/2026
24	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]	11/2017	1,255.17 -	1,255.17	95.24	03/2022 -	03/2022
25	BLOCK-B EXPANSION OPENCAST PROJECT - [N06000184]	7/2019	998.71 -	998.71	-	03/2023 -	03/2023
26	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]	5/2017	1,783.09 -	1,783.09	267.80	03/2021 -	03/2021
	<u>Singareni Colliers Company Limited</u>						
27	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]	12/2015	477.65 -	477.65	2.11	03/2020 -	03/2020
	<u>South-Eastern Coal Fields Limited</u>						
28	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]	3/2016	869.44 -	869.44	116.48	03/2021 -	03/2021
29	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	2,057.57	03/2023 -	03/2023
30	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	4.02	03/2023 -	03/2023
31	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
32	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]	6/2010	11,816.40 -	11,816.40	2,882.36	03/2023 -	03/2023
33	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	6.42	03/2023 -	03/2023
34	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	82.91	03/2020 -	03/2020
35	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	102.91	03/2022 -	03/2022
36	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
37	MAHAMAYA OPENCAST PROJECT - [N06000164]	5/2018	410.26 -	410.26	9.53	03/2026 -	03/2026
38	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
39	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	73.31	03/2020 -	03/2020
40	JHIRIA WEST OPENCAST PROJECT - [N06000166]	11/2018	389.97 -	389.97	-	03/2026 -	03/2026
41	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	75.96	03/2026 -	03/2026
42	MALACHUA OPENCAST PROJECT - [N06000139]	10/2015	488.33 -	488.33	27.10	03/2023 -	03/2023
43	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	52.43	03/2021 -	03/2021
44	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	104.06	03/2021 -	03/2021
	<u>Western Coal Fields Limited</u>						
45	VISHNUPURI UG TO OC MINE - [N06000178]	7/2018	195.57 -	195.57	2.94	03/2025 -	03/2025
46	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	213.24	03/2020 -	03/2020
47	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	121.74	03/2020 -	03/2020
48	GANDHIGRAM UG MINE - [N06000183]	8/2019	414.16 -	414.16	-	03/2026 -	03/2026
49	UKNI DEEP OC - [N06000179]	11/2018	318.14 -	318.14	146.45	03/2021 -	03/2021
50	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]	2/2017	328.00 -	328.00	160.15	03/2021 -	03/2021
51	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	413.13	03/2020 -	03/2020
52	BELLORA-NAIGAON DEEP OC - [N06000180]	11/2018	252.71 -	252.71	44.94	03/2021 -	03/2021
53	SAONER I UG TO OC PHASE I - [N06000177]	11/2016	162.10 -	162.10	50.56	03/2022 -	03/2022
54	KOLAR PIMPRI EXTENSION OC - [N06000160]	3/2017	362.73 -	362.73	319.93	03/2020 -	03/2020
55	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]	7/2016	409.87 -	409.87	20.30	03/2022 -	03/2022
56	BHANEGAON OC - [N06000121]	2/2015	187.94 -	409.68	128.90	03/2023 -	03/2023
57	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	210.32	03/2021 -	03/2021
58	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	319.76	235.33	03/2022 -	03/2022
59	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	182.76	03/2020 -	03/2020
60	DHANKASA UG (1.00 MTY) - [N06000155]	9/2016	458.07 -	458.07	20.86	03/2022 -	03/2022
61	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	268.58	03/2025 -	03/2025
	Total		74,841.58 -	75,064.12	20,071.50		

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>FERTILISERS</u>						
	<u>National Fertiliser Limited</u>						
62	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]	1/2018	239.81 -	239.81	134.46	11/2019 -	11/2019
63	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]	1/2018	215.92 -	215.92	117.03	11/2019 -	11/2019
64	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]	1/2018	218.83 -	218.83	119.23	11/2019 -	11/2019
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
65	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]	4/2018	426.72 -	426.72	197.47	04/2020 -	04/2020
	Total		1,101.28 -	1,101.28	568.19		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>National Building Construcion Corporation Ltd</u>						
66	AIIMS BILASPUR - [N21000028]	4/2018	1,351.00 -	1,351.00	137.87	09/2021 -	09/2021
	Total		1,351.00 -	1,351.00	137.87		
	<u>HEAVY INDUSTRY</u>						
	<u>Bharat Heavy Electricals Limited</u>						
67	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]	8/2016	1,554.00 -	1,554.00	335.03	09/2019 -	09/2019
	Total		1,554.00 -	1,554.00	335.03		
	<u>INFORMATION AND BROADCASTING</u>						
	<u>National Building Construcion Corporation Ltd</u>						
68	NATIONAL CENTRE OF EXCELLENCE FOR ANIMATION VISUAL EFFECTS GAMING AND COMICS - [N09000003]	12/2016	167.70 -	167.70	-	03/2020 -	03/2020
	Total		167.70 -	167.70	.00		
	<u>MINES</u>						
	<u>National Aluminum Company Limited (Nalco)</u>						
69	UTKAL D AND E COAL BLOCK - [N10000011]	5/2016	534.00 -	534.00	319.23	01/2020 -	01/2020
70	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	5,540.00 -	5,540.00	107.45	04/2021 04/2021	04/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
71	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]	11/2017	483.00 -	483.00	0.30	04/2021 04/2021	04/2021
72	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]	12/2015	355.00 -	355.00	31.92	11/2020 -	11/2020
	Total		6,912.00 -	6,912.00	458.90		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
73	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]	11/2018	248.55 -	248.55	22.86	06/2022 -	06/2022
74	MMPL PIPELINE REROUTING PROJECT - [N16000261]	4/2013	449.58 -	449.58	155.32	12/2019 -	12/2019
75	2G ETHANOL BIO REFINERY AT BARGARH - [N16000341]	8/2017	750.00 -	750.00	34.73	12/2020 -	12/2020
76	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]	9/2018	11,130.00 -	11,130.00	18.14	03/2023 -	03/2023
77	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL - [N16000365]	12/2017	1,524.06 -	1,524.06	13.73	12/2021 -	12/2021
78	PUNE POL STORAGE DEPOT - [N16000313]	8/2016	282.64 -	282.64	127.11	08/2020 -	08/2020
79	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364]	7/2017	580.20 -	580.20	38.21	02/2021 -	02/2021
80	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]	10/2018	206.26 -	206.26	0.98	03/2021 -	03/2021
	<u>Chennai Petroleum Corporation Limited</u>						
81	BS-VI PROJECTS - [N16000295]	9/2017	1,858.00 -	1,858.00	1,026.86	12/2019 -	12/2019
82	RE-LIQUIFIED NATURAL GAS - [N16000301]	8/2017	421.00 -	421.00	137.46	08/2020 -	08/2020
	<u>Gas Authority Of India Limited</u>						
83	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329]	10/2017	226.45 -	226.45	50.15	10/2022 -	10/2022
84	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]	7/2015	2,881.40 -	2,000.00	1,285.47	12/2020 -	12/2020
85	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]	7/2017	182.20 -	182.20	30.42	07/2022 -	07/2022
86	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]	3/2017	3,437.00 -	3,437.00	1,271.51	12/2020 -	12/2020
87	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]	10/2017	359.25 -	359.25	68.16	10/2022 -	10/2022
88	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]	9/2018	225.54 -	225.54	1.41	02/2021 -	02/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
89	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]	7/2017	243.53 -	243.53	52.38	07/2022 -	07/2022
90	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	287.49	125.82	04/2022 -	04/2022
91	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	2/2015	749.00 -	842.00	606.89	02/2020 -	02/2020
92	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR - [N16000330]	10/2017	221.45 -	221.45	46.15	10/2022 -	10/2022
93	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	3/2017	1,933.00 -	1,933.00	1,035.77	12/2020 -	12/2020
94	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	3/2017	1,740.00 -	1,740.00	275.95	12/2020 -	12/2020
95	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]	3/2017	2,433.00 -	2,433.00	1,441.96	12/2020 -	12/2020
96	BARAUNI-GUWAHATI PIPELINE - [N16000334]	6/2018	3,308.00 -	3,308.00	1,250.10	12/2021 -	12/2021
	<u>Hindustan Petroleum Corporation Limited</u>						
97	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	9/2017	2,677.00 -	2,677.00	894.02	03/2021 -	03/2021
98	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]	9/2015	4,199.00 -	5,060.00	2,754.00	03/2020 -	03/2020
99	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]	11/2017	255.00 -	255.00	75.50	11/2020 -	11/2020
100	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369]	12/2018	854.00 -	854.00	38.34	12/2022 -	12/2022
101	REDEVELOPMENT/ EXPANSION OF MEERUT DEPOT FOR ENHANCING PRODUCT HANDLING CAPACITY - [N16000366]	8/2016	154.84 -	154.84	120.67	11/2019 -	11/2019
102	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]	9/2016	1,879.00 -	1,879.00	1,476.87	06/2020 -	06/2020
103	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,928.00 -	20,928.00	6,455.02	07/2020 -	07/2020
104	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367]	6/2019	2,166.38 -	2,166.38	9.80	06/2022 -	06/2022
	<u>Indian Oil Corporation Limited</u>						
105	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]	2/2015	890.00 -	887.00	603.29	10/2019 -	10/2019
106	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]	4/2018	5,654.00 -	5,654.00	344.69	10/2021 -	10/2021
107	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]	12/2018	611.00 -	611.00	1.68	04/2022 -	04/2022
108	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]	3/2018	676.00 -	676.00	168.18	12/2021 -	12/2021
109	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT - [N16000363]	12/2018	278.60 -	278.60	-	06/2021 -	06/2021
110	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]	5/2019	3,361.00 -	3,361.00	325.72	08/2021 -	08/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
111	120 TMTA LPG BOTTLING PLANT AT GORAKHPUR UP - [N16000354]	3/2014	204.00 -	204.00	139.25	09/2019 -	09/2019
112	LPG BP PROJECT MOTIHARI - [N16000317]	5/2018	206.50 -	206.50	13.88	03/2021 -	03/2021
113	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]	5/2013	711.00 -	711.00	11.12	06/2020 -	06/2020
114	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]	11/2018	462.30 -	462.30	-	09/2021 -	09/2021
115	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]	10/2018	316.20 -	316.20	14.78	10/2021 -	10/2021
116	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]	8/2018	1,636.00 -	1,636.00	148.87	08/2020 -	08/2020
117	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]	4/2018	206.63 -	206.63	13.75	02/2020 -	02/2020
118	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]	10/2018	1,297.50 -	1,297.50	10.17	10/2021 -	10/2021
119	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]	9/2016	208.35 -	208.35	123.99	07/2020 -	07/2020
120	AUGMENTATION OF CTMPL - [N16000286]	12/2016	228.00 -	228.00	15.40	06/2020 -	06/2020
121	ADDITIONAL FACILITIES AT VIJAYAWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]	1/2015	342.00 -	342.00	-	03/2021 -	03/2021
122	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]	4/2016	1,021.00 -	1,021.00	4.45	12/2020 -	12/2020
123	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]	7/2018	189.00 -	189.00	9.15	01/2021 -	01/2021
124	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]	4/2018	522.00 -	522.00	142.71	03/2021 -	03/2021
125	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]	2/2016	2,582.00 -	2,582.00	1,557.14	11/2019 -	11/2019
126	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]	12/2017	199.36 -	199.36	9.39	10/2020 -	10/2020
127	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]	7/2014	247.00 -	247.00	-	03/2021 -	03/2021
128	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]	1/2019	909.00 -	909.00	16.17	01/2021 -	01/2021
129	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	1/2015	1,823.00 -	3,027.90	861.98	12/2020 -	12/2020
130	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	960.09	08/2021 -	08/2021
131	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]	5/2016	261.00 -	261.00	41.42	01/2021 -	01/2021
132	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309]	8/2017	1,342.00 -	1,342.00	6.30	08/2020 -	08/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
133	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]	8/2017	255.40 -	255.40	1.75	08/2020 -	08/2020
134	FUEL QUALITY UPGADATION (NSU,NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY - [N16000348]	6/2017	951.64 -	951.64	399.12	10/2019 -	10/2019
135	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]	10/2018	598.00 -	598.00	15.22	02/2020 -	02/2020
136	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]	6/2019	371.00 -	371.00	-	09/2022 -	09/2022
137	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]	8/2018	557.00 -	557.00	217.83	02/2020 -	02/2020
	<u>Oil & Natural Gas Corporation Limited</u>						
138	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]	4/2019	3,228.80 -	3,228.80	458.52	03/2022 -	03/2022
139	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]	2/2017	511.30 -	511.30	476.47	11/2019 -	11/2019
140	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]	2/2017	968.61 -	1,033.95	930.62	11/2019 -	11/2019
141	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]	2/2019	2,292.46 -	2,292.46	300.13	05/2021 -	05/2021
142	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]	5/2019	763.92 -	763.92	-	12/2020 -	12/2020
143	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) - [N16000335]	4/2018	766.37 -	766.37	449.88	12/2019 -	12/2019
144	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	1,162.56	392.39	03/2026 -	03/2026
145	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	7/2016	249.85 250.00	265.49	157.81	05/2020 -	05/2020
146	GAS COMPRESSOR PROJECT AT ANKLESHWAR ASSET (GCP-ANK) - [N16000371]	10/2018	156.67 -	156.67	-	03/2021 -	03/2021
	<u>Oil India Limited</u>						
147	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]	9/2016	571.66 -	571.66	200.97	12/2019 -	12/2019
148	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]	5/2016	406.00 -	406.00	88.85	10/2020 -	10/2020
149	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN - [N16000356]	6/2016	224.75 -	224.75	4.37	08/2020 -	08/2020
	Total		1,11,156.25 -	1,12,511.73	30,579.26		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
150	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000273]	12/2018	587.44 -	587.44	250.00	09/2020 -	09/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
151	TALAIPALLI COAL MINING PROJECT - [N18000266]	9/2015	3,004.00 -	3,004.00	1,610.00	11/2019 -	11/2019
152	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000274]	3/2019	349.00 -	349.00	125.00	11/2020 -	11/2020
153	PATRATU STPP-I (3X800MW) - [N18000275]	11/2017	18,668.00 -	18,668.00	2,004.32	03/2023 -	03/2023
154	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	11,148.86	8,619.60	01/2020 -	01/2020
	<u>Power Grid Corporation Of India Limited</u>						
155	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]	2/2017	195.05 -	195.05	120.83	02/2020 -	02/2020
156	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]	5/2016	14,733.37 -	14,733.37	8,796.37	11/2019 -	11/2019
157	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]	3/2017	283.72 -	283.72	193.70	11/2019 -	11/2019
158	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]	8/2017	1,931.39 -	1,931.39	1,054.28	02/2020 -	02/2020
159	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	3/2017	3,500.00 3,500.00	3,500.00	1,758.00	07/2020 -	07/2020
160	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]	11/2017	358.83 -	358.83	121.83	05/2020 -	05/2020
161	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]	3/2017	379.95 -	379.95	76.66	12/2019 -	12/2019
162	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]	2/2017	5,070.13 -	5,070.13	2,771.21	04/2020 -	04/2020
	<u>Satluj Jal Vidyut Nigam Limited</u>						
163	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]	3/2019	10,439.09 -	10,439.09	780.04	01/2024 -	01/2024
164	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	648.33	265.90	12/2021 -	12/2021
	<u>Thdc India Limited</u>						
165	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]	3/2019	11,089.42 -	11,089.42	521.82	09/2023 -	09/2023
166	AMELIA COAL MINE - [N18000252]	1/2017	2,104.21 -	1,587.16	307.48	09/2020 -	09/2020
	Total		83,212.44 -	83,973.74	29,377.04		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
167	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]	2/2015	2,449.91 -	2,449.91	165.28	03/2023 -	03/2023
168	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]	2/2016	9,968.00 -	9,968.00	-	03/2024 -	03/2024

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
169	PUNE-NASIK (265 KM) - [N22000354]	2/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024
170	DAUND - MANMAD (236 KM) - [N22000360]	2/2016	1,876.00 -	2,081.27	121.17	03/2023 -	03/2023
171	WARDHA-NANDED MAHARASHTRA - [N22000231]	4/2008	3,168.29 -	3,168.29	1,202.43	03/2023 -	03/2023
172	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]	2/2016	2,750.00 -	3,438.51	-	03/2024 -	03/2024
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
173	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	03/2020
	<u>East Central Railways</u>						
174	KOSI BRIDGE (NL), ECR - [220100304]	4/2002	499.41 -	516.02	397.11	03/2020 -	03/2020
	<u>East Coast Railway</u>						
175	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]	4/2015	2,499.71 -	3,382.95	373.22	03/2022 -	03/2022
	<u>North Central Railway</u>						
176	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	4/2015	668.70 668.00	680.00	330.00	03/2020 -	03/2020
177	JHANSI BINA DOUBLING - [N22000496]	9/2016	2,001.00 -	2,001.00	416.59	03/2021 -	03/2021
178	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]	3/2018	4,329.53 -	4,329.53	3.90	03/2023 -	03/2023
	<u>North East Frontier Railway</u>						
179	DIGARU-HOJAI (102 KM) - [N22000389]	4/2015	870.96 -	2,136.01	502.44	03/2021 -	03/2021
180	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	4/2010	906.46 -	6,000.00	261.76	03/2021 -	03/2021
181	MURKONGSELEK-PASIGHAT NL - [N22000208]	4/2011	414.84 -	661.00	122.05	03/2020 -	03/2020
182	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	4/2010	242.22 -	471.00	68.15	03/2020 -	03/2020
183	DIMAPUR-TIZIT NL - [N22000196]	4/2013	4,274.00 -	4,274.00	-	03/2020 -	03/2020
	<u>North Eastern Railway</u>						
184	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	3/2007	243.78 -	895.00	106.55	12/2021 -	12/2021
185	HATHUA-BHATNI (N L) (NER) - [220100319]	4/2005	230.03 -	230.03	277.14	12/2022 -	12/2022
186	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]	4/2016	1,900.00 -	1,277.06	-	01/2022 -	01/2022
187	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]	4/2016	600.00 -	600.00	25.24	01/2022 -	01/2022
	<u>Northern Railway</u>						
188	CHANDIGARH-BADDI - [N22000467]	4/2007	328.14 -	1,540.00	233.84	03/2023 -	03/2023
	<u>National High Speed Rail Corporation Limited</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
189	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]	12/2015	1,08,000.00 -	1,08,000.00	4,886.79	12/2023 12/2023	12/2023
	<u>Rail India Technical And Economic Service</u>						
190	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498]	2/2016	393.98 -	393.98	241.23	03/2020 -	03/2020
191	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	281.85	03/2021 -	03/2021
	<u>Rail Vikas Nigam Ltd.</u>						
192	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	773.94 -	773.94	413.71	12/2024 -	12/2024
193	VIJAYAWADA-GUDUR - [N22000369]	4/2015	3,246.26 -	3,548.67	1,072.89	12/2023 -	12/2023
194	DHASA-JETALSAR (GC) - [N22000141]	4/2012	644.38 -	644.38	352.02	03/2021 -	03/2021
195	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	1/1991	2,335.67 -	2,335.68	598.12	12/2024 -	12/2024
196	AHMEDABAD-BOTAD (GC) - [N22000140]	4/2012	975.62 -	1,082.32	994.30	12/2021 -	12/2021
197	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	3/2009	713.48 -	1,950.00	1,957.22	03/2020 -	03/2020
	<u>South Central Railway</u>						
198	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	4/2010	704.31 -	1,352.74	269.07	03/2020 -	03/2020
199	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	4/2017	119.73 185.00	184.97	3.67	03/2022 -	03/2022
	<u>South East Central Railway</u>						
200	ANUPPUR-KATNI - [N22000485]	4/2015	1,370.00 -	1,370.00	281.19	12/2021 12/2021	12/2021
201	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	9/2016	1,908.51 -	2,686.63	443.56	03/2023 03/2023	03/2023
	<u>South Western Railway</u>						
202	ARSIKERE-TUMKUR - [N22000332]	3/2015	578.00 -	578.00	509.07	03/2020 -	03/2020
203	YELAHANKA-PENUKONDA - [N22000328]	5/2015	860.43 -	860.43	697.21	03/2020 -	03/2020
	<u>Southern Railway</u>						
204	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]	2/2015	1,700.00 -	1,003.00	167.73	03/2022 -	03/2022
	<u>Western Railway</u>						
205	CHOTTAUDEPUR-DHAR(NL) - [N22000138]	4/2007	1,347.26 -	1,347.26	724.63	03/2022 03/2022	03/2022
206	SURENDRA NAGAR RAJKOT - [N22000392]	4/2015	1,002.39 -	1,002.39	378.38	03/2021 03/2021	03/2021
	Total		1,86,548.32 -	2,36,293.03	41,364.51		

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways</u>						
207	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777	11/2017	283.51 -	283.51	126.38	11/2019 -	11/2019
208	PUNE TO MALE VILLAGE - [N24001078	3/2018	228.31 -	228.31	13.50	12/2019 -	12/2019
209	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821	11/2017	257.34 -	238.00	41.09	11/2019 -	11/2019
210	BAMNI TO NAVAEGAON - [N24001110	9/2017	241.69 242.00	241.69	146.29	04/2020 -	04/2020
211	JALGAON TO BHADGAON - [N24001045	1/2018	307.54 308.00	307.54	124.59	11/2019 -	11/2019
212	ARDHAPUR TO HIMAYATNAGAR - [N24001079	12/2017	426.06 426.00	426.06	66.97	06/2020 -	06/2020
213	OMREGA TO AUSA - [N24001067	3/2018	272.04 272.00	272.04	124.24	12/2019 -	12/2019
214	MAHAD TO RAIGAD FORT - [N24001038	7/2018	237.40 -	237.40	8.34	05/2020 -	05/2020
215	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779	2/2018	418.88 -	418.88	88.00	02/2020 -	02/2020
216	KUSUMBA TO MALEGAON - [N24001109	3/2018	243.45 244.00	243.45	67.02	12/2019 -	12/2019
217	CHALISGAON TO NANDGAON - [N24001108	3/2018	206.97 207.00	206.97	78.89	12/2019 -	12/2019
218	BHOGAN KHURD TO KASHEDI - [N24001132	9/2017	743.21 743.00	743.21	131.87	06/2021 -	06/2021
219	BHADGAON TO CHALISGAON - [N24001047	1/2018	259.55 260.00	259.55	145.00	11/2019 -	11/2019
220	KOTHARI TO DHANORA - [N24001073	9/2018	301.38 301.00	301.38	41.00	08/2020 -	08/2020
221	NILAJPHATA TO BHANDARA - [N24001043	1/2018	420.63 421.00	420.63	17.60	05/2020 -	05/2020
222	KARWANDI TO RAJURI - [N24001058	3/2018	276.95 277.00	276.95	81.47	12/2019 -	12/2019
223	KUNDRAL TO WAZAR - [N24001077	1/2018	225.25 225.00	225.25	121.75	12/2019 -	12/2019
224	TASGAON TO SHIRDHON - [N24001054	1/2017	195.64 196.00	195.64	169.73	11/2019 -	11/2019
225	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774	12/2017	248.22 -	248.22	57.20	12/2019 -	12/2019
226	SANGOLA TO JATH - [N24001052	1/2018	257.38 257.00	257.38	61.15	12/2019 -	12/2019
227	SALAIKHURD TO TIRORA - [N24001042	1/2018	415.25 415.25	415.25	82.22	12/2019 -	12/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
228	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]	3/2018	336.21 336.00	336.21	64.66	12/2019 -	12/2019
229	MALEGAON TO RISOD - [N24001089]	2/2018	303.24 303.00	303.24	107.97	12/2019 -	12/2019
230	KARASWADA TO BAMBOLIM - [N24001005]	3/2017	852.67 -	852.67	108.04	12/2019 -	12/2019
231	MANGRUPHIR TO MAHAN - [N24001087]	3/2018	222.13 222.00	222.13	60.36	11/2019 -	11/2019
232	PATRADEVI TO KARASWADA 4L - [N24001004]	3/2017	634.32 -	634.32	102.33	05/2020 -	05/2020
233	NASRATPUR TO BARASGAON - [N24001112]	7/2016	406.54 407.00	406.54	142.00	09/2019 -	09/2019
234	JAHIRABAD TO LATUR - [N24001040]	1/2017	461.96 -	461.96	151.43	11/2019 -	11/2019
235	MANSAR TO SALAIKHURD - [N24001035]	1/2018	418.36 -	418.36	116.13	12/2019 -	12/2019
236	WARDHA TO ARVI - [N24001150]	2/2018	313.58 -	313.58	4.96	04/2020 -	04/2020
237	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]	3/2016	536.65 356.00	536.65	42.25	12/2019 -	12/2019
238	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]	11/2017	237.80 -	238.00	7.48	11/2019 -	11/2019
239	SHIVUR TO YEOLA - [N24001059]	3/2018	181.08 -	181.08	2.50	12/2019 -	12/2019
240	DHANGIPIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]	3/2018	217.14 217.00	217.14	66.77	02/2020 -	02/2020
241	JALGAON TO NANDURA - [N24001088]	3/2018	177.84 177.00	177.84	125.69	12/2019 -	12/2019
242	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]	5/2018	248.00 -	248.00	-	05/2020 -	05/2020
243	NALDURG TO AKKALKOT - [N24001051]	2/2018	274.50 275.00	274.50	61.39	12/2019 -	12/2019
244	KALMATH TO ZARAP - [N24001137]	9/2016	1,338.13 1,338.00	1,338.13	959.51	03/2020 -	03/2020
245	WADIGODRI TO DHANGRIPIMPRI - [N24001063]	3/2018	194.23 194.00	194.23	68.23	02/2020 -	02/2020
246	PAHUR TO BODHWAD - [N24001084]	1/2017	244.93 -	244.93	40.23	05/2020 -	05/2020
247	DEULGAON SAKARSHA TO MEHKAR - [N24001076]	3/2018	219.91 -	219.91	106.46	12/2019 -	12/2019
248	TALGAON TO KALMATH - [N24001136]	10/2016	904.70 905.00	904.70	604.05	03/2020 -	03/2020
249	LATUR TO PANGAON - [N24001066]	3/2018	336.47 336.00	336.47	109.48	12/2019 -	12/2019
250	PARBHANI TO GANGKHED - [N24001065]	3/2018	238.19 238.00	238.19	40.85	12/2019 -	12/2019
251	WASHIM TO DASTAPUR - [N24001068]	3/2018	165.51 -	165.51	35.45	12/2019 -	12/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
252	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]	3/2018	223.46 -	223.46	21.42	12/2019 -	12/2019
253	CHIKLI TO TAKARKHED - [N24001083]	3/2018	393.10 393.00	393.10	125.97	12/2019 -	12/2019
254	VITA TO NAGAJ - [N24001050]	3/2018	304.58 305.00	304.58	9.16	12/2019 -	12/2019
255	OSMANNAGAR TO KUNDRAL - [N24001075]	9/2017	344.25 344.00	344.25	33.02	08/2020 -	08/2020
256	NANDED TO JALKOT - [N24001069]	12/2017	456.93 457.00	456.93	54.50	09/2019 -	09/2019
257	KARAD TO VITA - [N24001049]	1/2018	344.85 245.00	344.85	68.04	12/2019 -	12/2019
258	KANTE TO WAKED - [N24001134]	3/2016	1,230.02 1,230.00	1,230.02	500.61	11/2019 -	11/2019
259	KHERDA TO NAGZARI - [N24001072]	3/2018	181.30 -	181.30	70.50	12/2019 -	12/2019
260	PALPHATA TO PHULAMBARI - [N24001060]	3/2018	227.19 227.00	227.19	60.23	12/2019 -	12/2019
261	WARDHA TO HINGAGHAT - [N24001098]	1/2018	216.90 217.00	216.90	45.00	12/2019 -	12/2019
262	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]	1/2019	264.50 -	264.50	-	03/2021 -	03/2021
263	CHIKALI TO DHAD - [N24001061]	3/2018	189.46 189.00	189.46	21.54	12/2019 -	12/2019
264	RISOD TO HINGOLI - [N24001149]	2/2018	355.99 -	355.99	112.97	12/2019 -	12/2019
265	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]	11/2017	232.81 -	232.81	59.44	11/2019 -	11/2019
266	ARNI TO NAIGAINBANDI - [N24001093]	12/2017	309.94 310.00	309.94	51.32	12/2019 -	12/2019
267	DASTAPUR TO KARANJA - [N24001070]	3/2018	182.63 -	182.63	83.40	12/2019 -	12/2019
268	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]	12/2017	200.34 -	200.34	31.00	12/2019 -	12/2019
269	SHAHAPUR PATGAON SECTION I - [N24001027]	1/2018	150.79 -	150.79	21.42	12/2019 -	12/2019
270	SELDOH TO PANVAR - [N24001097]	7/2018	404.33 404.00	404.33	30.19	05/2020 -	05/2020
271	PANCHARAL TO MANDANGHAR - [N24001107]	7/2018	381.08 302.00	381.08	13.00	05/2020 -	05/2020
272	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]	3/2018	294.87 295.00	294.87	12.30	12/2019 -	12/2019
273	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]	3/2018	256.15 -	256.15	15.50	12/2019 -	12/2019
274	PATGAON KHOPOLI SECTION I - [N24001028]	1/2018	170.00 -	170.00	39.57	12/2019 -	12/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
275	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772	12/2017	257.34 -	257.34	62.79	12/2019 -	12/2019
276	KHAMGAON TO DEULGAON SAKARSHA - [N24001074	3/2018	249.29 -	249.29	72.20	12/2019 -	12/2019
277	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778	11/2017	266.52 -	266.52	144.27	11/2019 -	11/2019
278	JALKOT TO TOGRI - [N24001071	7/2018	299.92 300.00	299.92	4.20	08/2020 -	08/2020
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
279	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862	4/2017	537.82 -	537.82	-	09/2019 -	09/2019
280	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857	4/2017	519.09 -	519.09	-	09/2019 -	09/2019
281	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859	4/2017	642.96 -	642.96	-	09/2019 -	09/2019
282	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861	4/2017	473.18 -	473.18	-	09/2019 -	09/2019
283	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858	4/2017	640.07 -	640.07	-	09/2019 -	09/2019
284	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863	4/2017	518.53 -	518.53	-	09/2019 -	09/2019
285	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864	4/2017	404.29 -	404.29	-	09/2019 -	09/2019
286	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865	4/2017	428.11 -	428.11	-	09/2019 -	09/2019
	<u>National Highways Authority Of India</u>						
287	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	3/2017	672.89 -	736.01	-	03/2020 -	03/2020
288	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	3/2017	2,064.99 -	2,447.00	1,653.62	03/2020 -	03/2020
289	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652	3/2017	848.45 -	848.45	73.46	03/2020 -	03/2020
290	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	3/2017	744.64 -	982.00	-	03/2020 -	03/2020
291	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670	3/2017	239.68 -	235.90	91.24	03/2020 -	03/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
292	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602	8/2016	1,664.20 -	1,664.20	657.08	04/2020 -	04/2020
293	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600	8/2016	1,388.34 -	2,525.80	1,449.00	09/2019 03/2020	09/2019
	<u>National Highways Development Project</u>						
294	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478	12/2015	957.54 -	957.54	467.50	02/2020 -	02/2020
295	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475	11/2015	628.45 -	628.45	252.21	01/2020 -	01/2020
	<u>Public Works Dept Of State</u>						
296	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907	3/2018	293.10 -	293.10	10.26	08/2020 -	08/2020
297	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884	3/2018	191.21 -	191.21	72.02	11/2019 -	11/2019
298	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906	3/2018	173.24 -	173.24	10.97	06/2020 -	06/2020
299	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879	3/2017	202.69 -	202.69	93.93	11/2019 -	11/2019
300	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941	3/2018	293.64 -	293.64	28.24	08/2020 -	08/2020
301	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204	7/2016	208.88 -	208.88	36.25	10/2019 -	10/2019
302	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987	1/2018	283.15 -	283.15	42.22	05/2020 -	05/2020
303	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909	10/2017	1,069.59 -	1,069.59	629.87	10/2019 -	10/2019
304	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984	1/2017	283.00 -	283.00	152.35	12/2019 -	12/2019
305	FOUR LANING WIDENING & STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (JAN - [N24001208	3/2018	288.30 -	288.30	0.34	08/2020 -	08/2020
306	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992	2/2018	426.52 -	426.52	225.51	04/2020 -	04/2020
307	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131	3/2018	212.99 -	212.99	80.47	06/2020 -	06/2020
308	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993	3/2018	322.81 -	322.81	1.66	09/2020 -	09/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
309	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991	2/2018	220.28 -	220.28	37.58	11/2019 -	11/2019
310	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206	3/2018	263.89 -	263.89	67.69	04/2020 -	04/2020
311	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152	9/2018	160.00 -	160.00	0.50	09/2021 -	09/2021
312	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209	3/2016	296.50 -	296.50	0.51	09/2020 -	09/2020
313	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175	10/2016	167.62 -	167.62	42.15	12/2020 -	12/2020
314	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178	11/2016	336.25 -	336.25	62.64	09/2019 -	09/2019
315	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994	3/2018	626.76 -	626.76	80.66	07/2020 -	07/2020
316	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996	1/2017	605.08 -	605.08	273.88	10/2019 -	10/2019
317	REHABILITATION AND UPGRADATION OF HARPALPUR - SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942	3/2016	208.50 -	208.50	123.66	11/2019 -	11/2019
318	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883	3/2018	254.30 -	254.30	52.85	10/2020 -	10/2020
319	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA - [N24001139	10/2016	218.94 219.00	218.94	86.07	03/2020 -	03/2020
320	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141	3/2016	240.30 240.00	240.30	194.01	01/2020 -	01/2020
321	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880	2/2018	426.18 -	426.18	219.94	09/2020 -	09/2020
322	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905	3/2018	322.48 -	322.48	48.73	07/2020 -	07/2020
323	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197	3/2018	351.00 -	351.00	0.48	06/2021 -	06/2021
324	REHABILITATION AND UPGRADATION OF ALLAHABAD - MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203	10/2016	218.90 -	218.90	23.37	03/2020 -	03/2020
325	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. - [N24001174	10/2016	235.31 -	235.31	91.38	11/2020 -	11/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
326	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]	2/2018	206.13 -	206.13	127.86	06/2020 -	06/2020
327	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]	3/2018	185.18 -	185.18	2.86	02/2020 -	02/2020
328	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]	10/2016	172.63 -	172.63	45.02	12/2020 -	12/2020
329	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]	1/2018	230.03 -	230.03	127.98	12/2019 -	12/2019
330	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]	3/2018	170.57 -	170.57	46.23	11/2020 -	11/2020
331	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]	11/2016	215.16 215.00	215.16	157.79	09/2019 -	09/2019
332	R AND U FROM KM 385.00 TO KM 420.000 TO 2- LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404 - [N24001205]	12/2016	209.10 -	209.10	54.18	10/2019 -	10/2019
333	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]	1/2017	196.52 -	196.52	103.12	10/2019 -	10/2019
334	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]	2/2018	218.70 -	218.70	37.75	11/2020 -	11/2020
335	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180]	3/2019	237.51 -	237.51	-	12/2022 -	12/2022
336	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]	2/2018	294.13 -	294.13	39.44	11/2019 -	11/2019
337	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C - [N24000999]	11/2016	230.34 -	230.34	178.39	10/2019 -	10/2019
338	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]	3/2017	217.35 -	217.35	35.10	11/2020 -	11/2020
339	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927]	3/2018	293.64 -	293.64	28.24	08/2020 -	08/2020
340	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148]	3/2016	599.34 -	599.34	449.19	01/2020 -	01/2020
341	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]	10/2016	171.90 -	171.90	11.75	08/2020 -	08/2020
342	REHABILITATION AND UPGRADATION OF BARAICH - SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA - [N24001202]	3/2016	388.83 -	388.83	280.17	12/2019 -	12/2019
	Total		51,330.98 -	53,128.01	15,845.45		

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>SHIPPING AND PORTS</u>						
	<u>Inland Waterways Authority Of India</u>						
343	JAL MARG VIKAS PROJECT - [N25000072]	1/2018	4,200.00 -	5,369.18	1,400.95	03/2023 03/2023	03/2023
	Total		4,200.00 -	5,369.18	1,400.95		
	<u>STEEL</u>						
	<u>Steel Authority Of India Limited (Sail)</u>						
344	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E - [N12000121]	12/2018	263.36 -	263.36	11.32	09/2020 -	09/2020
	Total		263.36 -	263.36	11.32		
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
345	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]	11/2017	171.72 -	171.72	32.00	03/2020 -	03/2020
346	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]	10/2017	271.90 -	271.90	33.56	11/2019 -	11/2019
347	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]	11/2017	238.56 -	238.56	63.42	05/2020 -	05/2020
348	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST) - [N28000112]	9/2017	150.29 -	150.29	2.58	03/2020 -	03/2020
349	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]	1/2019	790.79 -	800.00	2.56	03/2022 -	03/2022
	<u>Madhya Pradesh Metro Rail Co Limited</u>						
350	BHOPAL METRO RAIL - [N28000124]	11/2018	6,941.40 -	6,941.40	34.12	02/2023 -	02/2023
351	INDORE METRO RAIL - [N28000125]	11/2018	7,500.80 -	7,500.80	42.62	02/2023 -	02/2023
	<u>National Building Construcion Corporation Ltd</u>						
352	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,439.23	3,246.53	11/2019 -	11/2019
	Total		20,329.46 -	20,513.90	3,457.39		
	<u>WATER RESOURCES</u>						
	<u>Brahmaputra Board</u>						
353	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]	3/2017	233.57 -	233.57	32.20	12/2019 -	12/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		233.57	233.57	32.20		
	Grand Total		5,48,235.62	6,03,470.44	1,44,334.44		

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Annexure - V

(September 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [N020100044]	09/2003	3,492.00 -	6,840.00	09/2010 -	10/2021	95.88
	<u>Nuclear Power Corporation Of India Limited</u>						
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	12/2015 -	06/2020	44.69
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]	10/2009	12,320.00 -	17,079.00	12/2016 -	12/2020	38.63
	Total		27,271.00 -	40,499.00			
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI [N04000083]	12/2016	859.86 -	860.00	03/2021 -	03/2021	.02
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]	09/2015	338.93 -	339.00	06/2019 -	12/2019	.02
	Total		1,513.40 -	1,640.33			
	<u>COAL</u>						
	<u>Eastern Coal Fields Limited</u>						
7	RANIGANJ MASTER PLAN - [N06000163]	08/2009	2,661.73 -	5,186.24	08/2019 -	-	94.84
	<u>Neyveli Lignite Corporation</u>						
8	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	06/2011	5,907.11 -	7,080.41	12/2015 -	12/2019	19.86
9	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80	11/2021 -	11/2021	.00
	<u>Singareni Colliers Company Limited</u>						
10	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86
11	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	03/2012 -	03/2024	80.24
12	KAKATIYAKHANI OPENCASE-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	03/2019 -	03/2020	11.42

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
13	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 -	473.22	03/2015 -	03/2021	5.85
14	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	03/2015 -	03/2021	114.60
	<u>South-Eastern Coal Fields Limited</u>						
15	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	03/2015 -	03/2020	201.44
	<u>Western Coal Fields Limited</u>						
16	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	313.34	03/2021 -	03/2024	12.85
17	BHANEGAON OC - [N06000121]	02/2015	187.94 -	409.68	03/2023 -	03/2023	117.98
18	ADASA UG TO OC - [N06000133]	08/2015	288.90 -	333.43	03/2023 -	03/2024	15.41
	Total		28,387.67 -	33,223.79			
	<u>FERTILISERS</u>						
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
19	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	11/2016 -	09/2019	5.89
	Total		197.79 -	209.44			
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation Ltd</u>						
20	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	02/2013	414.11 -	513.89	11/2013 -	10/2020	24.10
21	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	09/2014	505.58 -	523.00	03/2018 -	-	3.45
22	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]	12/2017	156.56 -	156.65	- -	02/2020	.06
	Total		1,076.25 -	1,193.54			
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
23	HALDIA LPG IMPORT FACILITY - [N16000223]	03/2015	694.00 -	1,097.54	10/2018 -	12/2019	58.15
24	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29 -	5,245.96	08/2018 -	11/2019	14.33
25	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]	12/2015	1,112.00 -	1,507.24	06/2019 -	02/2022	35.54
	<u>Gas Authority Of India Limited</u>						

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
26	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	02/2015	749.00 -	842.00	02/2020 -	02/2020	12.42
27	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II [N16000285]	06/2009	2,915.00 2,915.00	3,049.47	12/2012 -	02/2022	4.61
	<u>Hindustan Petroleum Corporation Limited</u>						
28	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]	11/2011	310.00 -	370.00	03/2013 -	-	19.35
29	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]	09/2015	4,199.00 -	5,060.00	03/2020 -	03/2020	20.50
	<u>Indian Oil Corporation Limited</u>						
30	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	10/2017 -	-	17.66
31	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	01/2015	1,823.00 -	3,027.90	12/2020 -	12/2020	66.09
32	PARADIP HYDERABAD PIPELINE - [N16000194]	01/2015	2,321.00 -	3,338.00	12/2020 -	08/2020	43.82
33	ENMORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	05/2016	4,497.00 -	6,025.00	12/2018 -	02/2021	33.98
	<u>Indian Strategic Petroleum Reserves Ltd</u>						
34	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	-	70.49
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
35	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]	10/2015	135.00 171.00	170.70	03/2019 -	10/2019	26.44
36	SEA WATER DESALINATION PLANT - [N16000319]	11/2017	581.00 -	621.00	03/2020 -	09/2020	6.88
	<u>Oil & Natural Gas Corporation Limited</u>						
37	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) [N16000127]	06/2010	202.94 -	345.92	01/2014 -	11/2019	70.45
38	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) [N16000128]	03/2011	861.79 -	1,683.06	05/2013 -	12/2019	95.30
39	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	12/2019	29.42
40	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS [N16000213]	12/2015	3,190.69 -	3,247.19	04/2018 -	05/2020	1.77
41	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	823.27 -	910.23	03/2023 -	03/2022	10.56
42	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	07/2016	249.85 250.00	265.49	05/2020 -	05/2020	6.26
43	DEVELOPMENT OF B-147 FIELD - [N16000292]	02/2017	546.15 -	565.15	11/2019 -	03/2020	3.48

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
44	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]	02/2017	968.61 -	1,033.95	11/2019 -	11/2019	6.75
45	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]	02/2017	4,006.83 -	4,475.92	05/2021 -	12/2021	11.71
46	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]	02/2019	3,660.71 -	3,740.05	04/2021 -	05/2021	2.17
	<u>Oil India Limited</u>						
47	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	438.84	03/2017 -	12/2019	24.47
48	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	-	37.72
49	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	01/2018	543.91 -	682.90	02/2020 -	06/2020	25.55
	Total		43,862.64 -	54,016.41			
	<u>POWER</u>						
	<u>National Hydro-Electric Power Corporation</u>						
50	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	9,997.11	09/2009 -	12/2021	155.06
51	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	19,496.34	09/2010 -	-	210.19
	<u>National Thermal Power Corporation</u>						
52	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	12,865.92	01/2018 -	03/2020	10.55
53	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	5,867.38	03/2013 -	01/2021	96.99
54	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 -	13,740.53	12/2018 -	09/2020	9.64
55	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,164.05	06/2019 -	09/2021	5.55
56	RAMMAM-III HEPP (3X40 MW) - [N18000178]	09/2014	1,381.84 -	1,592.34	09/2019 -	02/2022	15.23
57	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	9,996.59	07/2012 -	09/2020	86.75
58	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	17,304.00	05/2018 -	03/2021	33.47
59	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]	04/2012	9,750.89 -	12,176.28	02/2017 -	06/2020	24.87
60	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	21,312.11	10/2011 -	08/2021	145.16
61	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	10/2017 -	03/2020	7.55

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
62	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	07/2012	1,527.00 -	1,801.07	08/2017 -	-	17.95
63	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	03/2015	9,870.51 -	11,148.86	01/2020 -	01/2020	12.95
64	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	10/2017 -	-	7.41
	<u>North East Electric Power Corporation</u>						
65	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	7,927.34	12/2009 06/2016	10/2019	217.49
	<u>Power Grid Corporation Of India Limited</u>						
66	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]	10/2008	4,824.12 -	5,071.94	10/2012 -	12/2019	5.14
67	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	14,719.10	08/2013 -	03/2022	32.24
68	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	04/2016 -	11/2019	38.61
69	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	546.36	11/2016 -	03/2020	4.61
70	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	02/2014	196.58 -	225.28	02/2016 -	06/2019	14.60
71	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP - [N18000180]	01/2015	268.80 -	340.88	03/2018 -	06/2019	26.82
72	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03	07/2017 -	10/2019	27.92
73	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	06/2014 -	10/2019	31.17
74	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,187.32	11/2008 -	-	22.93
75	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,072.36	12/2018 -	12/2020	90.82
76	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,880.36	12/2018 -	12/2020	34.61
	<u>Thdc India Limited</u>						
77	DHUKWAN SMALL HYDRO PROJECT - [N18000189]	05/2011	195.42 -	294.60	02/2014 -	12/2019	50.75
78	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	4,397.80	06/2013 -	12/2022	76.51
79	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	5,024.35	02/2016 -	06/2022	203.22
	Total		1,54,828.95 -	2,29,232.99			
	<u>RAILWAYS</u>						

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>Central Railways</u>						
80	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89 -	1,377.48	03/2021 -	03/2022	73.73
81	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 -	305.00	03/2019 -	12/2019	65.71
82	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 -	3,712.50	03/2021 -	03/2022	63.44
83	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 -	5,341.68	03/2024 -	03/2024	120.28
84	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 -	3,438.51	03/2024 -	03/2024	25.04
85	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	03/2023 -	03/2023	10.94
	<u>Container Corporation Of India</u>						
86	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 -	235.00	03/2019 -	12/2020	.21
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
87	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]	10/2006	11,589.00 30,357.00	28,181.00	- -	-	143.17
88	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]	11/2007	16,592.00 51,101.00	51,101.00	03/2020 -	03/2020	207.99
	<u>East Central Railways</u>						
89	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	03/1999	1,033.07 -	3,376.00	- -	03/2021	226.79
90	HAIJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	04/2003	528.65 -	2,066.78	- -	03/2023	290.95
91	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	477.88 283.95	751.55	03/2012 -	03/2020	57.27
92	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	324.73 -	1,050.00	03/2012 -	03/2020	223.35
93	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	614.45	- -	03/2022	277.26
94	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	499.41 -	516.02	03/2020 -	03/2020	3.33
95	SAMASTIPUR-DARBANGHA - [N22000329]	05/2015	380.00 -	519.33	- -	02/2023	36.67
96	CONSTRUCTION OF ROBS IN THE STATE OF BIHAR - [N22000344]	07/2004	599.63 674.00	674.00	12/2007 -	-	12.40
97	KODERMA-TILAIYA (NL), ECR - [220100305]	04/2002	459.91 -	1,625.87	- -	03/2021	253.52
98	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 -	549.75	- -	-	32.26
99	BIHTA-AURANGABAD (NL) - [N22000170]	04/2008	326.20 -	2,995.01	- -	03/2024	818.15
100	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	325.00 -	735.20	- -	03/2021	126.22

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
101	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	378.56 -	2,609.00	- -	03/2022	589.19
102	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	1,006.00	- -	-	376.78
103	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]	04/2004	372.14 -	1,470.50	- -	03/2021	295.15
104	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]	04/2009	548.00 -	819.01	03/2020 -	03/2022	49.45
105	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	425.17	- -	01/2020	99.60
106	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	546.71	07/2014 -	-	64.60
107	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 -	1,215.54	03/2021 -	03/2022	63.37
108	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 -	1,185.73	03/2021 -	03/2022	62.06
109	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]	04/1998	180.82 -	726.31	- -	10/2019	301.68
110	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN- BIHARSHARIF, - [N22000476]	04/1991	329.39 -	1,483.14	- -	12/2021	350.27
<u>East Coast Railway</u>							
111	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07	06/2021 -	06/2024	137.80
112	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	2,923.13 -	3,791.66	03/2009 -	06/2024	29.71
113	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	1,111.99 -	1,539.28	02/2019 -	03/2022	38.43
114	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,160.83	03/2020 -	03/2023	.07
115	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 -	238.03	03/2020 -	03/2021	52.77
116	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]	04/2015	2,499.71 -	3,382.95	03/2022 -	03/2022	35.33
117	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	04/2015	701.61 -	810.02	11/2018 -	03/2022	15.45
<u>Eastern Railways</u>							
118	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,619.48	03/2019 12/2009	03/2025	36.22
119	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 -	1,425.44	02/2013 -	03/2024	134.80
120	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 -	527.54	- -	03/2025	44.46

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
121	HANSDIHA-GODDA NL - [N22000236]	04/2011	542.18 -	693.80	03/2020 -	03/2021	27.96
122	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]	04/2011	175.80 -	245.41	- -	03/2021	39.60
123	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	04/2011	299.60 -	335.62	03/2017 -	03/2026	12.02
124	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI- BAHRAHAT NL - [N22000240]	04/2010	494.54 -	494.59	03/2005 -	03/2025	.01
125	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR- MINAKHAN VIA GHATAKAPUR NL - [N22000241]	04/2000	297.47 -	298.22	- -	03/2025	.25
126	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHNACHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	499.96 -	680.68	02/2012 -	03/2025	36.15
127	MONIGRAM- NIMTITA - [N22000301]	04/2012	250.93 -	310.70	- -	03/2024	23.82
128	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	04/2012	255.64 -	272.20	- -	09/2021	6.48
129	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP- BUDAKHALI AND CHANDRANAG - [N22000216]	04/1987	406.99 -	545.70	03/2006 -	03/2025	34.08
130	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]	04/2007	450.00 -	1,261.34	- -	03/2025	180.30
131	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 -	260.10	- -	03/2025	51.19
132	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	2,137.81	03/2022 -	03/2025	133.39
133	BANDEL-BOINCHI 3RD LINE - [N22000221]	04/2011	288.35 -	382.90	- -	03/2020	32.79
134	PIRPAINTI-BHAGALPUR - [N22000222]	04/2011	261.38 -	471.81	- -	05/2019	80.51
135	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]	04/2001	923.52 -	995.10	03/2016 -	03/2025	7.75
136	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]	04/2005	595.51 -	769.40	03/2017 -	03/2025	29.20
<u>Indian Railway Construction Company Limited</u>							
137	GEVRA ROAD PENDRA ROAD - [N22000488]	02/2014	2,288.00 -	4,970.11	03/2022 -	12/2022	117.23
<u>Metropolitan Rapid Transport Projects</u>							
138	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM- NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
139	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	2,980.41	03/2004 -	03/2021	501.57

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
140	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 -	734.01	06/2013 -	-	48.06
141	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	03/2013	4,874.58 -	8,574.97	03/2016 -	06/2021	75.91
	<u>North Central Railway</u>						
142	ETAHWAH-MAINPURI (NL),NCR - [220100318]	04/1997	120.00 -	346.00	12/2008 -	-	188.33
143	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96 -	3,845.60	03/2022 -	12/2024	32.02
144	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	04/2015	668.70 668.00	680.00	03/2020 -	03/2020	1.69
	<u>North East Frontier Railway</u>						
145	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	297.32 -	614.00	03/2019 -	03/2020	106.51
146	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 -	5,021.45	03/2014 -	03/2022	109.80
147	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	1,180.19 -	4,541.00	12/2008 -	03/2021	284.77
148	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 -	12,524.00	03/2011 -	03/2020	181.17
149	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	385.20 -	1,532.00	03/2019 -	03/2020	297.72
150	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	532.87 -	2,145.00	03/2019 -	03/2020	302.54
151	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	2,326.52 -	4,600.00	03/2015 -	10/2021	97.72
152	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	333.76 -	360.00	- -	03/2022	7.86
153	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,084.69	12/2015 -	-	204.95
154	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00 -	2,496.67	03/2019 -	-	38.86
155	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	380.00	- -	03/2022	71.62
156	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 -	650.00	03/2020 -	12/2021	14.11
157	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	906.46 -	6,000.00	03/2021 -	03/2021	561.92
158	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00	03/2020 -	03/2020	94.45
159	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	03/2021	63.25

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
160	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84 -	661.00	03/2020 -	03/2020	59.34
161	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	04/1999	819.23 -	1,871.00	- -	-	128.39
162	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	314.00 -	728.00	03/2019 -	03/2020	131.85
163	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 -	2,136.01	03/2021 -	03/2021	145.25
164	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	04/2016	602.27 -	612.00	12/2021 -	03/2020	1.62
165	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]	02/1999	380.60 -	1,871.00	04/2010 -	-	391.59
<u>North Eastern Railway</u>							
166	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	142.45 -	228.40	- -	-	60.34
167	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10
168	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 -	1,409.09	- -	-	358.99
169	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 -	895.00	12/2021 -	12/2021	267.13
170	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	01/2019 -	01/2020	61.80
171	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 -	644.00	- -	-	.16
172	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	04/2016 -	06/2020	.16
173	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]	04/2017	1,343.00 -	1,476.15	01/2018 -	-	9.91
174	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]	04/2016	602.50 -	714.34	- -	-	18.56
<u>North Western Railway</u>							
175	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	886.41	02/2019 -	03/2021	116.16
176	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	685.99	03/2020 -	04/2022	14.33
177	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]	05/2015	873.71 -	1,980.21	- -	-	126.64
178	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	348.55	12/2019 -	06/2020	41.64
179	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	4,079.15	- -	-	95.85

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
180	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	294.90	10/2018 -	10/2019	24.47
181	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]	04/2013	822.00 -	1,099.54	- -	-	33.76
182	PUSHKAR-MERTA - [N22000151]	04/2013	323.00 -	432.22	- -	-	33.81
183	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	303.56	11/2019 -	05/2020	42.26
184	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	410.00	02/2019 -	05/2020	69.36
	<u>Northern Railway</u>						
185	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	197.17	- -	03/2024	25.87
186	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	694.00	12/2011 -	03/2021	141.81
187	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]	04/2007	336.91 -	800.00	- -	03/2022	137.45
188	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63	- -	06/2020	57.68
189	UNCHAHAH-AMETHI - [N22000294]	04/2012	1,229.00 -	1,230.00	- -	03/2023	.08
190	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,010.00	07/2012 -	03/2024	346.67
191	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	27,949.00	11/2002 -	06/2022	1,017.96
192	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 -	1,540.00	03/2023 -	03/2023	369.31
193	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 -	845.58	03/2016 -	03/2021	35.29
	<u>Rail Vikas Nigam Ltd.</u>						
194	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	1,185.64 -	1,844.47	12/2017 -	03/2020	55.57
195	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	385.00	03/2009 03/2009	12/2019	188.58
196	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	2,966.99 -	7,000.00	12/2026 -	12/2025	135.93
197	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 -	2,900.00	03/2023 -	03/2024	36.34
198	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2025	7.78
199	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95
200	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	975.62 -	1,082.32	12/2021 -	12/2021	10.94

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
201	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2020	29.06
202	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.67	12/2023 -	12/2023	9.32
203	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,200.00	03/2019 -	03/2020	29.45
204	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE- GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 -	1,950.00	03/2020 -	03/2020	173.31
205	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 -	2,335.68	12/2024 -	12/2024	.00
206	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 -	1,500.00	03/2020 -	03/2021	58.22
207	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 -	1,120.00	03/2019 -	06/2022	18.78
	<u>Railway Electrification</u>						
208	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	-	60.77
	<u>South Central Railway</u>						
209	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 -	2,120.16	03/2009 -	03/2023	102.85
210	MANUGURU-RAMAGUNDAM - [N22000259]	04/2013	1,112.00 -	2,911.84	- -	-	161.86
211	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,856.95 -	2,200.00	03/2023 -	03/2024	18.47
212	BHADRACHALAM-KOVVUR - [N22000264]	04/2012	923.23 -	1,787.00	- -	-	93.56
213	CUMBUM-PRODDATUR - [N22000282]	04/2013	829.00 -	1,599.39	- -	-	92.93
214	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	704.31 -	1,352.74	03/2020 -	03/2020	92.07
215	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	164.36 -	1,050.00	02/2009 -	-	538.84
216	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	458.25 -	458.26	- -	-	.00
217	KONDAPALLI-KOTHAGUDEM - [N22000364]	04/2013	723.00 -	997.09	- -	-	37.91
218	MANMAD-PARBHANI-NANDED-SECUNDERABAD- GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	04/2017	119.73 185.00	184.97	03/2022 -	03/2022	54.49
	<u>South East Central Railway</u>						
219	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	1,413.76	- -	10/2019	268.37
220	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	511.86 -	1,756.92	04/2020 -	12/2020	243.24

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
221	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,908.51 -	2,686.63	03/2023 -	03/2023	40.77
222	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438]	04/2010	585.93 -	1,300.44	02/2019 -	06/2020	121.94
223	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00 -	860.92	12/2021 -	03/2023	275.95
224	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]	04/2008	872.00 -	1,226.51	12/2019 -	10/2019	40.65
225	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	04/2015	1,973.00 -	1,973.66	03/2021 -	12/2022	.03
	<u>South Eastern Railway</u>						
226	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	-	160.76
227	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	377.00	12/2016 -	12/2019	153.41
228	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	620.00	- -	03/2025	131.89
229	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	651.00 -	1,009.00	03/2015 -	-	54.99
230	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	-	53.44
231	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	358.68	12/2018 -	06/2020	38.92
232	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	1,312.96	03/2020 -	06/2020	35.38
233	BONDAMUNDA RANCHI DOUBLING - [N22000396]	03/2016	1,724.20 -	1,993.24	03/2021 -	12/2021	15.60
234	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 -	2,373.00	03/2003 -	03/2030	130.97
	<u>South Western Railway</u>						
235	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	12/2023	24.09
236	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	12/2023	57.65
237	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	12/2023	14.14
238	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	12/2023	12.38
239	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 -	1,870.41	03/2019 -	03/2021	15.84
240	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78 -	889.52	03/2017 -	03/2020	37.96
	<u>Southern Railway</u>						
241	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI [N22000079]	09/2007	724.69 -	2,072.50	02/2019 -	02/2020	185.98

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
242	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	227.40 -	900.00	- -	-	295.78
243	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	582.83 -	2,300.00	- -	-	294.63
244	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	303.98 -	980.00	03/2020 -	03/2021	222.39
245	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	1,566.00 -	2,815.62	- -	-	79.80
246	ATTIPPATTU PUTTUR - [N22000184]	04/2008	151.84 -	1,105.00	02/2019 -	-	627.74
247	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	2,300.00	- -	-	339.33
248	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
249	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17
250	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	457.08	- -	-	69.20
251	ERODE-PALANI - [N22000199]	04/2008	288.57 -	1,140.00	- -	-	295.05
252	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	03/2020	173.71
253	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	931.98 -	951.24	- -	03/2020	2.07
254	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70 -	1,800.00	03/2019 -	12/2019	1,391.30
255	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM [N22000373]	10/2013	187.26 -	231.67	04/2014 -	03/2020	23.72
256	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	02/1996	268.87 -	950.00	03/2005 -	-	253.33
257	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00 -	1,182.31	03/2020 -	06/2021	55.57
	<u>West Central Railway</u>						
258	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60 -	2,909.99	03/2021 -	03/2023	585.35
259	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35
260	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13 -	1,247.64	03/2022 -	09/2022	114.32
	<u>Western Railway</u>						
261	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	3,503.69 -	3,860.40	03/2022 -	03/2023	10.18

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
262	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]	04/2006	117.36 196.95	202.35	03/2011 -	03/2017	72.42
263	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	03/2022	1.06
264	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	04/2008	829.74 -	1,310.23	03/2020 -	03/2021	57.91
265	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	858.96	03/2019 -	03/2022	167.87
266	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]	02/1991	551.51 -	809.07	03/2019 -	03/2020	46.70
	Total		1,78,466.58 -	3,92,821.78			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Dept Of Road Transport & Highways</u>						
267	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]	03/2015	280.16 -	290.59	- -	-	3.72
	<u>Ministry Of Road Transport And Highways</u>						
268	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]	12/2011	156.26 227.00	247.95	- -	-	58.68
269	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]	03/2015	258.97 -	268.92	08/2015 -	-	3.84
270	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]	03/2015	157.18 162.00	162.00	07/2015 -	-	3.07
271	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]	01/1991	675.00 -	780.77	- -	-	15.67
272	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]	01/1991	282.41 -	322.01	08/2016 -	-	14.02
273	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]	01/1991	358.22 -	377.64	10/2016 -	-	5.42
274	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]	03/2014	191.50 192.00	192.00	05/2016 -	12/2019	.26
275	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]	08/2013	171.96 172.00	172.00	06/2016 -	11/2019	.02

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
276	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782	03/2018	460.73 -	461.00	- -	-	.06
277	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820	11/2017	237.80 -	238.00	11/2019 -	11/2019	.08
278	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928	10/2015	333.21 -	355.89	12/2015 -	12/2019	6.81
279	BHOKAR TO SARSAM - [N24001128	02/2017	295.09 -	295.99	07/2019 -	-	.31
280	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144	10/2013	445.89 653.00	653.29	03/2017 -	09/2019	46.51
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
281	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676	12/2016	138.93 155.00	155.00	01/2017 -	01/2020	11.57
282	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695	04/2017	388.00 -	447.37	10/2017 -	-	15.30
	<u>National Highways Authority Of India</u>						
283	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 -	525.00	02/2009 -	07/2019	87.50
284	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	340.14	04/2009 -	08/2019	70.23
285	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279	12/2003	167.64 -	408.77	11/2008 -	01/2014	143.84
286	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	255.23	11/2008 -	08/2013	64.62
287	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049	12/2003	160.00 -	167.98	05/2008 -	06/2019	4.99
288	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	655.17	07/2009 -	10/2018	234.27
289	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,967.50	11/2011 -	03/2020	167.82
290	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063	12/2003	217.61 -	360.84	04/2010 -	07/2019	65.82
291	NALBARI T BIJNI (AS-7) - [N24000048	12/2003	208.00 -	230.00	04/2008 -	03/2020	10.58
292	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233	04/2014	1,266.60 -	1,544.00	09/2016 -	09/2019	21.90
293	NASHRI- CHANANI - [N24000162	05/2011	2,159.00 -	2,519.00	06/2015 -	-	16.67
294	AHMEDABAD TO VADODARA SECTION - [N24000222	01/2013	2,125.24 -	2,521.24	12/2015 -	-	18.63
295	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224	10/2012	1,928.22 -	2,945.00	04/2015 -	-	52.73

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
296	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435	10/2015	531.13 -	727.00	05/2018 -	09/2020	36.88
297	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441	10/2015	593.26 -	636.24	05/2018 -	06/2020	7.24
298	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459	06/2015	845.24 -	941.00	- -	10/2019	11.33
299	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494	05/2013	1,055.00 -	1,601.77	11/2015 -	-	51.83
300	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503	10/2015	447.29 -	746.43	12/2017 -	12/2019	66.88
301	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551	03/2016	1,587.49 -	2,982.00	04/2019 -	10/2019	87.84
302	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572	05/2016	364.56 -	392.00	- -	12/2019	7.53
303	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600	08/2016	1,388.34 -	2,525.80	09/2019 -	09/2019	81.93
304	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609	09/2015	771.18 -	7,558.00	- -	-	880.06
305	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622	09/2016	950.69 -	1,108.00	08/2019 -	12/2020	16.55
306	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631	11/2016	290.73 -	315.00	- -	03/2019	8.35
307	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638	11/2012	605.84 -	722.46	07/2018 -	02/2020	19.25
308	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.71 -	1,310.00	03/2020 -	08/2020	10.58
309	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	03/2017	744.64 -	982.00	03/2020 -	03/2020	31.88
310	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657	03/2017	1,030.44 -	1,065.51	03/2020 -	05/2020	3.40
311	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	03/2017	988.34 -	1,043.28	03/2020 -	08/2020	5.56
312	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659	03/2017	1,059.73 -	1,071.00	03/2017 -	11/2020	1.06
313	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	03/2017	1,098.06 -	1,160.64	03/2020 -	08/2020	5.70
314	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	03/2017	754.54 -	756.27	03/2020 -	04/2020	.23

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
315	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	03/2017	672.89 -	736.01	03/2020 -	03/2020	9.38
316	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 -	1,187.10	03/2020 -	05/2020	13.97
317	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669	03/2017	165.50 -	172.16	03/2020 -	-	4.02
318	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 -	1,420.00	03/2020 -	03/2021	10.24
319	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 -	2,447.00	03/2020 -	03/2020	18.50
320	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 -	1,177.00	03/2020 -	07/2020	41.54
321	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	03/2020 -	06/2020	44.39
322	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704	09/2017	1,124.11 -	1,232.76	09/2017 -	06/2020	9.67
323	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713	12/2017	404.94 -	448.18	- -	10/2020	10.68
324	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784	02/2018	1,424.77 -	1,853.42	- -	-	30.09
325	SIX-LANING OF BANGALORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787	02/2018	1,995.34 -	2,400.00	- -	11/2021	20.28
326	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789	02/2018	2,177.80 -	2,450.00	- -	-	12.50
327	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801	02/2018	1,052.21 -	1,449.00	- -	01/2021	37.71
328	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807	03/2018	1,532.62 -	2,499.00	03/2021 -	04/2021	63.05
329	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814	03/2018	1,029.96 -	1,261.05	- -	03/2021	22.44
330	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829	03/2018	1,016.92 -	1,071.00	- -	04/2021	5.32
331	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830	03/2018	2,065.96 -	2,169.00	- -	-	4.99

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
332	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831	03/2018	1,294.47 -	1,296.00	- -	-	.12
333	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839	03/2018	634.70 -	931.21	- -	07/2021	46.72
334	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841	03/2018	795.50 -	799.30	- -	07/2021	.48
335	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853	03/2018	642.13 -	807.00	- -	12/2020	25.68
	<u>National Highways Development Project</u>						
336	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371	10/2013	445.89 -	653.29	03/2017 -	09/2019	46.51
337	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388	11/2013	497.05 -	881.05	05/2017 -	05/2020	77.26
	<u>Public Works Dept Of State</u>						
338	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306	11/2010	624.41 -	992.67	03/2011 -	12/2019	58.98
339	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307	12/2011	156.63 276.00	276.00	02/2012 -	-	76.21
340	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308	08/2010	193.69 -	327.92	10/2010 -	12/2019	69.30
341	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311	03/2012	207.03 -	389.45	05/2012 -	-	88.11
342	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314	01/2013	182.28 -	269.14	02/2013 -	12/2019	47.65
343	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	09/2017 -	12/2019	36.24
344	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391	11/2015	889.24 -	904.82	- -	-	1.75
345	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396	11/2010	470.20 -	630.36	02/2011 -	-	34.06
346	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407	10/2015	333.21 -	353.89	11/2015 -	-	6.21

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
347	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411	11/2014	218.31 -	307.47	02/2018 -	-	40.84
348	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415	08/2010	195.04 -	377.99	10/2010 -	06/2020	93.80
349	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531	01/1991	319.68 -	369.77	- -	-	15.67
350	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O - [N24000871	08/2014	600.87 720.97	720.97	11/2017 -	05/2019	19.99
351	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873	08/2014	823.20 937.76	937.76	11/2017 -	06/2019	13.92
352	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874	03/2016	271.17 291.20	291.20	11/2018 -	11/2019	7.39
353	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND) - [N24000885	03/2016	160.27 -	213.97	08/2019 -	08/2021	33.51
354	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887	06/2016	236.78 -	263.26	08/2019 -	08/2021	11.18
355	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889	04/2014	279.70 398.22	398.52	08/2017 -	07/2019	42.48
356	NAGAU-BIKANER OF NH-11 (2L+PS) UNDER PPP. - [N24000954	01/2012	378.07 -	478.73	01/2014 -	-	26.62
357	DEVELOPMENT AND OPERATION OF BIKANER-SURATGARH SECTION OF NH-15 BY 2L+PS IN THE STATE OF RAJASTHAN - [N24000956	03/2009	501.00 -	671.54	09/2013 -	-	34.04
358	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181	08/2010	186.96 -	305.61	09/2014 -	12/2019	63.46
	Total		63,969.35 -	89,108.69			
	<u>SHIPPING AND PORTS</u>						
	<u>Inland Waterways Authority Of India</u>						
359	JAL MARG VIKAS PROJECT - [N25000072	01/2018	4,200.00 -	5,369.18	03/2023 -	03/2023	27.84
	Total		4,200.00 -	5,369.18			
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
360	NMDC INTEGRATED STEEL PLANT - [N12000086]	01/2010	15,525.00 -	23,140.00	05/2015 -	07/2020	49.05
	Total		15,525.00 -	23,140.00			
	<u>TELECOMMUNICATIONS</u>						
	<u>Bharat Sanchar Nigam Limited</u>						
361	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]	01/2018	231.80 -	240.10	10/2018 -	12/2019	3.58
	<u>Department Of Telecommunication</u>						
362	NETWORK FOR SPECTRUM - [N26000101]	03/2012	13,334.00 -	24,664.00	07/2015 -	05/2020	84.97
	Total		13,565.80 -	24,904.10			
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
363	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]	02/2014	388.00 -	488.28	05/2017 -	10/2019	25.85
364	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	2,000.00	10/2019 -	03/2021	64.04
365	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]	06/2014	157.84 -	169.16	03/2017 -	-	7.17
366	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	06/2017 -	10/2020	.57
367	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]	12/2008	114.26 266.00	266.00	12/2013 -	10/2019	132.80
368	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]	12/2016	549.31 -	559.47	07/2019 -	02/2020	1.85
369	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]	01/2019	790.79 -	800.00	03/2022 -	03/2022	1.16
	<u>Chennai Metro Rail Ltd</u>						
370	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]	02/2009	14,600.00 -	19,058.00	12/2015 -	-	30.53
	<u>Hindustan Steelwork Construction Limited</u>						
371	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]	12/2007	202.61 227.00	227.00	12/2016 -	-	12.04

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(September 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
372	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]	10/2011	175.49 206.71	206.71	12/2016 -	-	17.79
373	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]	05/2005	768.88 1,070.97	1,113.34	02/2014 -	-	44.80
374	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	03/2007	149.73 173.00	175.94	12/2015 -	-	17.50
	<u>Kochi Metro Rail Corporation Ltd</u>						
375	KOCHI METRO RAIL PROJECT - [N28000081]	07/2012	5,181.79 -	5,687.79	07/2017 -	12/2019	9.77
	<u>National Building Construcion Corporation Ltd</u>						
376	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	06/2012	4,264.00 -	4,439.23	11/2019 -	11/2019	4.11
	Total		29,058.09 -	35,689.91			
	<u>WATER RESOURCES</u>						
	<u>Polavaram Project Authority</u>						
377	POLAVARAM IRRIGATION PROJECT - [N30000002]	02/2009	10,151.04 -	55,548.87	03/2020 -	06/2021	447.22
	Total		10,151.04 -	55,548.87			
	Grand Total		5,72,073.56	9,86,598.03			

Details of Delayed Projects w.r.t. Original Schedule

Annexure - VI

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
	<u>Bhavini Limited</u>									
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI, TAMIL NADU	09/2003	3,492.00	6,840.00	5,821.38	09/2010	10/2021	133	95.88	
	<u>Nuclear Power Corporation Of India Limited</u>									
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 16,580.00	16,580.00	14,137.00	12/2015	06/2020	54	44.69	
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 17,079.00	17,079.00	11,387.00	12/2016	12/2020	48	38.63	
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL, TAMIL NADU	03/2013	39,849.00	39,849.00	15,706.00	11/2020	11/2023	36	0	
	Total		67,120.00	80,348.00	47,051.38					
	<u>CIVIL AVIATION</u>									
	<u>Airport Authority Of India Limited</u>									
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI, TRIPURA	09/2015	338.93	339.00	213.50	06/2019	12/2019	6	.02	
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, A & N ISLANDS	10/2013	314.61	441.33	85.79	09/2018	06/2020	21	40.28	
7	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPORT - [N04000076]AAI, DELHI	11/2016	233.38	233.38	84.73	04/2020	12/2020	8	0	
8	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA - [N04000080]AAI, WEST BENGAL	01/2016	219.91	219.91	61.61	03/2020	12/2020	9	0	
9	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI - [N04000074]AAI, TAMIL NADU	06/2018	2,467.00	2,467.00	213.17	02/2022	08/2022	6	0	
	Total		3,573.83	3,700.62	658.80					

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>COAL</u>									
	<u>Bharat Coking Coal Limited</u>									
10	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82	269.82	180.83	04/2014	11/2019	67	0	
11	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45	289.45	257.56	05/2014	03/2020	70	0	
	<u>Central Coal Fields Limited</u>									
12	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51	163.51	106.41	03/2011	03/2021	120	0	
13	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68	264.68	181.17	03/2012	03/2021	108	0	
14	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85	510.85	362.49	03/2016	03/2021	60	0	
15	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46	162.46	90.78	03/2014	03/2021	84	0	
16	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	706.40	706.40	354.93	07/2012	03/2022	116	0	
	<u>Eastern Coal Fields Limited</u>									
17	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05	1,055.05	510.31	03/2018	10/2020	31	0	1. Rehabilitation of PAFs: Progress of R&R activity delayed due to disputes among villagers for selection of rehab. site and resistance by villagers in shifting.
	<u>Mahanadi Coal Fields Limited</u>									
18	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96	302.96	302.96	03/2010	03/2020	120	0	
19	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.10	490.10	501.82	03/2017	03/2020	36	0	
20	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA	05/2014	337.66	337.66	183.98	03/2019	03/2020	12	0	
21	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA	06/2014	289.03	289.03	75.85	03/2018	03/2020	24	0	
22	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28	207.28	228.90	03/2012	03/2021	108	0	
23	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53	479.53	390.94	03/2013	03/2021	96	0	
24	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77	457.77	539.59	03/2013	03/2022	108	0	
25	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08	172.08	347.15	03/2010	03/2022	144	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
26	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA	05/2014	479.15 -	479.15	200.65	03/2019 -	03/2022	36	0	
	<u>Neyveli Lignite Corporation</u>									
27	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 7,080.41	7,080.41	6,730.63	12/2015 -	12/2019	48	19.86	
	<u>Singareni Colliers Company Limited</u>									
28	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78 -	209.78	154.58	03/2015 -	03/2020	60	0	
29	RG OC -III EXTENSION (PHASE - II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	135.62	06/2015 -	03/2020	57	0	
30	KALYANIKHANI OPENCAS T PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	384.32	103.95	07/2016 -	03/2020	44	-7.91	
31	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 -	415.37	166.43	03/2016 -	03/2020	48	-3.5	
32	KAKATIYAKHANI OPENCAS T-2 PROJECT - [N06000129]SCCL,TELANGANA	05/2015	397.09 -	442.42	92.46	03/2019 -	03/2020	12	11.42	
33	KOYAGUDEM OPENCAS T PROJECT - [N06000146]SCCL,TELANGANA	10/2015	426.79 -	426.79	.72	03/2018 -	03/2020	24	0	
34	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	164.04	119.59	03/2015 -	03/2021	72	-32.3	
35	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	349.28	8.00	03/2015 -	03/2021	72	114.6	
36	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	473.22	18.35	03/2015 -	03/2021	72	5.85	
37	KAKATIYAKHANI OPENCAS T III PROJECT PHASE-1 - [N06000161]SCCL,TELANGANA	03/2017	413.84 -	413.84	54.51	03/2019 -	03/2022	36	0	
38	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	489.62	343.10	03/2012 -	03/2023	132	16.86	
39	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	448.86	286.19	03/2012 -	03/2024	144	80.24	
	<u>South-Eastern Coal Fields Limited</u>									
40	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	459.49	193.40	03/2015 -	03/2020	60	201.44	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
41	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	2.88	03/2014 -	03/2020	72	0	
42	BAROUD OC EXPANSION (RCE)-3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56 -	258.56	180.07	03/2016 -	03/2020	48	0	
43	AMERA OC RCE - [N06000123]SECL,CHHATISGARH	02/2015	335.97 -	335.97	51.25	03/2018 -	03/2020	24	0	
44	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	192.55	03/2014 -	03/2021	84	0	
	<u>Western Coal Fields Limited</u>									
45	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA	08/2015	288.90 -	333.43	21.02	03/2023 -	03/2024	12	15.41	
46	KAMPTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA	11/2015	277.65 -	313.34	116.34	03/2021 -	03/2024	36	12.85	
	Total		18,538.74 -	20,501.47	13,787.96					
	<u>FERTILISERS</u>									
	<u>Rashtriya Chemical & Fertiliser Limited</u>									
47	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79 -	209.44	174.52	11/2016 -	09/2019	34	5.89	
	Total		197.79 -	209.44	174.52					
	<u>INFORMATION AND BROADCASTING</u>									
	<u>Central Public Works Department</u>									
48	FILM AND TELEVISION INSTITUTE ARUNACHAL PRADESH - [N09000002]CPWD,ANDHRA PRADESH	11/2016	204.32 -	204.32	-	02/2019 -	11/2019	9	0	
	Total		204.32 -	204.32	.00					
	<u>STEEL</u>									
	<u>National Mineral Development Corporation (Nmdc)</u>									
49	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH	01/2010	15,525.00 -	23,140.00	16,064.29	05/2015 07/2020	07/2020	62	49.05	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>Rastrya Ispat Nigam Limited</u>									
50	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH	04/2014	1,682.85 -	1,682.85	1,227.53	09/2018 10/2019	10/2019	13	0	No
51	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH	12/2011	2,858.00 -	2,500.00	1,400.76	12/2017 10/2019	10/2019	22	-12.53	No
52	CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH	08/2015	320.66 -	320.66	220.91	08/2018 10/2019	10/2019	14	0	NO
	<u>Steel Authority Of India Limited (SAIL)</u>									
53	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA	04/2015	3,127.30 -	3,127.30	3,031.06	04/2018 11/2019	11/2019	19	0	
54	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND	05/2015	1,154.18 -	1,154.18	963.95	12/2017 11/2019	11/2019	23	0	
55	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	1,034.01	436.08	10/2017 06/2020	06/2020	32	0	
56	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND	11/2016	262.87 -	262.87	104.85	06/2019 06/2020	06/2020	12	0	
	Total		25,964.87 -	33,221.87	23,449.43					
	<u>PETROLEUM</u>									
	<u>Bharat Petroleum Corporation Limited</u>									
57	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA	11/2014	4,588.29 5,245.96	5,245.96	3,711.38	08/2018 11/2019	11/2019	15	14.33	
58	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL,WEST BENGAL	03/2015	694.00 1,097.54	1,097.54	700.96	10/2018 12/2019	12/2019	14	58.15	
59	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA	02/2016	3,313.00 3,288.96	3,288.96	1,151.10	02/2020 10/2020	10/2020	8	-.73	
60	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 -	678.00	5.57	02/2017 -	10/2021	56	0	
61	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA	12/2015	1,112.00 1,507.24	1,507.24	525.00	06/2019 02/2022	02/2022	32	35.54	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>Gas Authority Of India Limited</u>									
62	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL, GUJARAT	04/2016	327.78 -	200.00	146.50	04/2018 -	10/2019	18	-38.98	
63	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]GAIL, HARYANA	08/2018	286.42 -	286.42	1.93	08/2020 09/2020	09/2020	1	0	
64	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL, MULTI STATE	06/2009	2,915.00 2,915.00	3,049.47	2,524.91	12/2012 -	02/2022	110	4.61	
	<u>Hindustan Petroleum Corporation Limited</u>									
65	180 TMTA NEW LPG PLANT AT PATALGANGA (DIST RAIGAD), MAHARASHTRA - [N16000315]HPCL, MAHARASHTRA	06/2017	249.26 -	249.26	60.45	06/2020 -	09/2021	15	0	
66	120 TMTA NEW LPG PLANT AT BARHI JHARKHAND STATE - [N16000316]HPCL, JHARKHAND	06/2017	161.50 -	161.50	17.78	06/2020 -	09/2021	15	0	
	<u>Indian Oil Corporation Limited</u>									
67	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR), CACHAR, ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL, ASSAM	06/2016	423.00 -	423.00	263.70	08/2019 -	09/2019	1	0	
68	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]IOCL, ODISHA	05/2016	429.00 -	429.00	311.78	01/2019 -	12/2019	11	0	
69	BS-VI PROJECT AT PANIPAT REFINERY - [N16000325]IOCL, HARYANA	12/2017	3,529.00 -	3,529.00	1,720.28	07/2019 -	12/2019	5	0	
70	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]IOCL, UTTAR PRADESH	01/2018	666.64 -	666.64	431.71	09/2019 -	01/2020	4	0	
71	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY - [N16000322]IOCL, WEST BENGAL	05/2018	2,934.40 -	2,934.40	1,653.76	09/2019 -	01/2020	4	0	
72	BS-VI PROJECT AT BONGAIGAON REFINERY - [N16000320]IOCL, ASSAM	05/2018	1,222.00 -	1,222.00	563.53	09/2019 -	02/2020	5	0	
73	BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]IOCL, GUJARAT	03/2018	3,380.00 -	3,380.00	2,102.63	09/2019 -	03/2020	6	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
74	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]IOCL,MADHYA PRADESH	08/2017	236.00 -	236.00	24.15	06/2020 -	08/2020	2	0	
75	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	299.12	07/2018 -	10/2020	27	0	
76	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND	02/2017	160.10 -	160.10	41.22	02/2020 -	10/2020	8	0	
77	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT	10/2017	906.00 -	906.00	93.08	02/2020 -	10/2020	8	0	
78	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU	05/2016	4,497.00 6,025.00	6,025.00	499.65	12/2018 -	02/2021	26	33.98	
79	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL, WEST BENGAL	04/2017	163.02 -	163.02	50.84	04/2020 -	03/2021	11	0	
80	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00 -	212.00	38.55	01/2021 -	04/2021	3	0	
81	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA	12/2016	161.59 -	161.59	38.29	12/2019 -	07/2021	19	0	
82	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH	08/2018	466.00 -	466.00	84.34	04/2021 -	07/2021	3	0	
83	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	466.43	30.95	10/2020 -	08/2021	10	0	
84	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 -	348.00	30.75	01/2021 -	10/2021	9	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
85	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	318.80	40.06	08/2021 -	11/2021	3	0	
86	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	355.00	14.07	04/2022 -	02/2023	10	0	
	<u>Mangalore Refinery And Petrochemicals Limited</u>									
87	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]MANGALORE REFIN,KARNATAKA	10/2015	135.00 170.70	170.70	156.65	03/2019 10/2019	10/2019	7	26.44	
88	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA	09/2016	1,810.00 1,810.00	1,810.00	823.40	12/2019 07/2020	07/2020	7	0	
89	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA	11/2017	581.00 -	621.00	84.47	03/2020 -	09/2020	6	6.88	
	<u>Oil & Natural Gas Corporation Limited</u>									
90	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]ONGC,ANDHRA PRADESH	04/2017	420.76 -	407.45	239.45	09/2018 09/2019	09/2019	12	-3.16	
91	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI	08/2014	6,086.08 5,842.31	5,842.31	4,784.88	05/2019 10/2019	10/2019	5	-4.01	
92	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 345.92	345.92	146.58	01/2014 -	11/2019	70	70.45	
93	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 -	2,378.86	2,147.00	03/2013 12/2019	12/2019	81	-3.5	
94	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 -	1,683.06	1,322.31	05/2013 12/2019	12/2019	79	95.3	
95	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	1,908.01	03/2015 12/2019	12/2019	57	29.42	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
96	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA	11/2014	6,068.80 -	5,296.93	4,758.62	04/2019 12/2019	12/2019	8	-12.72	
97	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]ONGC,MAHARASHTRA	01/2015	4,619.94 -	4,619.94	4,360.59	12/2017 03/2020	03/2020	27	0	
98	DEVELOPMENT OF B-147 FIELD - [N16000292]ONGC,MAHARASHTRA	02/2017	546.15 565.15	565.15	442.18	11/2019 03/2020	03/2020	4	3.48	
99	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA	08/2015	2,818.88 -	2,818.88	2,230.96	03/2019 05/2020	05/2020	14	0	
100	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA	12/2015	3,190.69 -	3,247.19	2,225.67	04/2018 05/2020	05/2020	25	1.77	
101	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	650.82 -	650.82	394.21	03/2019 05/2020	05/2020	14	0	
102	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]ONGC,MAHARASHTRA	02/2019	3,660.71 3,740.05	3,740.05	126.66	04/2021 -	05/2021	1	2.17	
103	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH	03/2016	34,012.00 -	34,012.00	3,411.92	06/2020 -	08/2021	14	0	
104	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]ONGC,MAHARASHTRA	02/2017	4,006.83 -	4,475.92	2,796.50	05/2021 12/2021	12/2021	7	11.71	
105	HEERA REDEVELOPMENT - PHASE III - [N16000360]ONGC,MAHARASHTRA	05/2019	2,494.68 -	2,494.68	-	12/2021 -	03/2022	3	0	
	<u>Oil India Limited</u>									
106	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM	07/2011	350.00 -	350.00	2.06	01/2019 -	09/2019	8	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
107	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	438.84	230.43	03/2017 -	12/2019	33	24.47	
108	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM	01/2018	543.91 -	682.90	8.97	02/2020 -	06/2020	4	25.55	
	Total		1,13,827.55 -	1,18,174.58	49,779.56					
	<u>POWER</u>									
	<u>National Hydro-Electric Power Corporation</u>									
109	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	9,997.11	7,642.51	09/2009 -	12/2021	147	155.05	
	<u>National Thermal Power Corporation</u>									
110	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	12/2012	11,846.00 -	12,739.82	12,457.15	10/2017 03/2020	03/2020	29	7.55	
111	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	03/2013	11,638.55 -	12,865.92	12,188.01	01/2018 03/2020	03/2020	26	10.55	
112	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC,ODISHA	05/2016	1,885.13 -	1,885.13	527.90	12/2018 -	03/2020	15	0	
113	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC,WEST BENGAL	12/2016	529.68 -	529.68	140.10	11/2018 -	03/2020	16	0	
114	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	12,176.28	9,794.00	02/2017 06/2020	06/2020	40	24.87	
115	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH	09/2014	9,188.98 -	9,188.98	6,502.04	07/2019 03/2020	07/2020	12	0	
116	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA	02/2014	12,532.44 -	13,740.53	9,726.03	12/2018 02/2020	09/2020	21	9.64	
117	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	9,996.59	7,918.78	07/2012 -	09/2020	98	86.75	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
118	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 5,867.38	5,867.38	4,182.37	03/2013 12/2020	01/2021	94	96.99	
119	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 17,304.00	17,304.00	13,970.00	05/2018 12/2021	03/2021	34	33.47	
120	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA	01/2016	10,598.98 -	10,598.98	5,557.96	11/2020 06/2021	06/2021	7	0	
121	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 21,312.11	21,312.11	16,453.44	10/2011 08/2021	08/2021	118	145.16	
122	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 -	15,164.05	9,221.99	06/2019 09/2019	09/2021	27	5.55	
123	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL	09/2014	1,381.84 -	1,592.34	486.24	09/2019 02/2022	02/2022	29	15.23	
	<u>North East Electric Power Corporation</u>									
124	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 7,927.34	7,927.34	7,579.17	12/2009 10/2019	10/2019	118	217.49	
	<u>Power Grid Corporation Of India Limited</u>									
125	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL,RAJASTHAN	07/2016	1,429.38 -	1,429.38	1,045.19	01/2019 07/2019	09/2019	8	0	
126	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	639.46	564.32	06/2014 -	10/2019	64	31.17	
127	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 -	260.03	193.57	07/2017 -	10/2019	27	27.92	
128	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	1,891.41	1,263.11	04/2016 -	11/2019	43	38.61	
129	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE	01/2015	871.62 -	871.62	582.02	10/2017 -	11/2019	25	0	
130	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA	04/2016	844.64 -	844.64	435.06	04/2019 -	11/2019	7	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
131	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE	09/2016	562.25 -	562.25	414.25	03/2019 -	11/2019	8	0	
132	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE	10/2016	608.24 -	608.24	413.61	04/2019 -	11/2019	7	0	
133	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE	12/2015	3,654.00 -	3,654.00	3,427.57	04/2019 -	11/2019	7	0	
134	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	5,071.94	4,565.74	10/2012 -	12/2019	86	5.14	
135	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	213.02	04/2016 -	12/2019	44	0	
136	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	5,151.37	3,153.93	03/2018 -	12/2019	21	0	
137	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	197.40	83.07	03/2018 -	12/2019	21	0	
138	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	1,394.52	427.71	05/2017 -	12/2019	31	0	
139	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE	05/2016	3,519.59 -	3,519.59	2,502.91	05/2019 -	12/2019	7	0	
140	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE	10/2016	408.46 -	408.46	288.56	01/2019 -	12/2019	11	0	
141	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE	02/2017	322.30 -	322.30	158.10	02/2019 -	12/2019	10	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
142	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE	03/2017	337.75 -	337.75	92.75	06/2019 -	12/2019	6	0	
143	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT	05/2017	175.64 -	175.64	100.00	09/2018 -	12/2019	15	0	
144	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 -	186.17	107.75	07/2019 -	12/2019	5	0	
145	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT	12/2017	193.14 -	193.14	97.26	06/2019 -	12/2019	6	0	
146	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL	04/2016	454.11 -	454.11	291.64	04/2018 -	01/2020	21	0	
147	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE	09/2017	198.49 -	198.49	83.31	09/2019 -	02/2020	5	0	
148	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 -	546.36	466.42	11/2016 -	03/2020	40	4.61	
149	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	808.63	525.58	01/2018 -	03/2020	26	0	
150	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	235.53	124.27	06/2019 -	03/2020	9	0	
151	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA	05/2017	445.89 -	445.89	285.22	02/2019 -	03/2020	13	0	
152	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	9,072.36	1,301.58	12/2018 -	12/2020	24	90.82	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
153	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	6,880.36	1,641.35	12/2018 -	12/2020	24	34.61	
154	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	14,719.10	12,814.08	08/2013 -	03/2022	103	32.24	
	<u>Thdc India Limited</u>									
155	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 -	294.60	310.08	02/2014 -	12/2019	70	50.75	
156	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 -	5,024.35	3,047.08	02/2016 -	06/2022	76	203.22	Renewal of lease for 3.0 Ha land at Asena Quarry and Transfer of additional 05 Ha. Forest land and permission for mining are pending. It needs to be expedited.
157	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	4,397.80	1,770.91	06/2013 -	12/2022	114	76.51	1) There have been frequent hindrances by local villagers since mobilization of works in Jan 2014. Local hindrances have minimized in VPHEP with the strong intervention of MoP and support of District Administration. Still regular support of Distt. Administration is required for smooth and unobstructed execution of the project works. 2) Approval of Gadi quarry and crusher plant is pending with District Administration/ GoUK.
	Total		1,75,240.00 -	2,34,057.76	1,67,138.71					
	<u>HEALTH AND FAMILY WELFARE</u>									
	<u>HII Infra Tech Services Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
158	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	785.00	244.66	04/2020 -	06/2020	2	0	
159	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	703.00	184.93	06/2020 -	08/2020	2	0	
160	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 -	875.00	39.27	05/2021 -	10/2021	5	0	
	<u>Hospital Services Consultancy Corporation</u>									
161	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	272.19	140.58	03/2019 -	10/2019	7	0	
	<u>Hospital Services Consultancy Corporation Ltd</u>									
162	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	204.44	188.00	05/2017 -	09/2019	28	0	
163	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	152.95	118.23	02/2018 -	09/2019	19	0	
164	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	363.99	166.19	05/2018 -	09/2019	16	0	
165	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	274.19	169.93	03/2019 -	10/2019	7	0	
166	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL	08/2017	355.15 -	355.15	148.84	03/2019 -	03/2020	12	0	
167	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	513.89	147.00	11/2013 -	10/2020	83	24.1	
	Total		4,400.02 -	4,499.80	1,547.63					
	RAILWAYS									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>Central Railways</u>									
168	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 199.12	305.00	269.39	03/2019 12/2019	12/2019	9	65.71	
169	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50 -	3,712.50	2,380.30	03/2021 -	03/2022	12	63.44	
170	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89 -	1,377.48	308.67	03/2021 -	03/2022	12	73.73	
171	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19 -	1,272.19	296.03	03/2022 -	03/2023	12	0	
172	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02 -	540.02	235.70	03/2022 -	03/2024	24	0	
173	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 -	1,035.16	90.49	03/2022 -	03/2024	24	0	
174	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 -	637.95	58.36	03/2023 -	03/2024	12	0	
	<u>Container Corporation Of India</u>									
175	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00 -	305.00	261.28	03/2019 -	12/2019	9	0	
176	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	343.00	222.83	03/2019 -	12/2019	9	0	
177	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	174.00	151.24	03/2019 -	02/2020	11	0	
178	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	493.17	439.80	03/2018 -	03/2020	24	0	
179	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32 -	346.32	286.78	03/2019 -	03/2020	12	0	
180	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	235.00	11.11	03/2019 -	12/2020	21	.21	
	<u>East Central Railways</u>									
181	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	528.57	107.81	03/2019 -	12/2019	9	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
182	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [N220100240] ECR, BIHAR	04/1997	324.73 898.53	1,050.00	1,040.00	03/2012 -	03/2020	96	223.35	
183	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N220000002] ECR, BIHAR	04/1996	477.88 751.55	751.55	673.69	03/2012 -	03/2020	96	57.27	
184	HAJIPUR - BACHAWARA - [N22000334] ECR, MULTI STATE	05/2015	678.54 678.54	678.54	492.44	03/2019 -	02/2021	23	0	
185	RAMNA - SINGRAULI DOUBLING - [N22000417] ECR, UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	517.46	03/2020 -	03/2021	12	0	
186	KIUL - GAYA DOUBLING PROJECT - [N22000349] ECR, BIHAR	12/2015	1,200.20 1,200.20	1,200.20	397.14	03/2020 -	10/2021	19	0	
187	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS (NEPAL) GC - [N22000181] ECR, BIHAR	04/2009	548.00 -	819.01	489.11	03/2020 -	03/2022	24	49.45	
188	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472] ECR, BIHAR	04/2016	744.04 1,215.54	1,215.54	63.74	03/2021 -	03/2022	12	63.37	
189	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473] ECR, BIHAR	04/2016	731.64 1,185.73	1,185.73	32.31	03/2021 -	03/2022	12	62.06	
190	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350] ECR, BIHAR	12/2015	1,491.47 -	1,491.47	438.38	03/2020 -	12/2022	33	0	
<u>East Coast Railway</u>										
191	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319] ECR, ODISHA	03/2012	155.81 -	238.03	226.50	03/2020 -	03/2021	12	52.77	
192	SAMBALPUR-TALCHER DOUBLING - [N22000315] ECR, ODISHA	03/2011	1,111.99 -	1,539.28	924.93	02/2019 -	03/2022	37	38.43	
193	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380] ECR, ODISHA	04/2015	701.61 -	810.02	122.59	11/2018 -	03/2022	40	15.45	
194	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381] ECR, ODISHA	04/2015	1,172.92 -	1,172.92	397.91	12/2018 03/2022	03/2022	39	0	
195	BHADRAK - NERGUNDI 3RD LINE - [N22000316] ECR, ODISHA	03/2013	843.04 -	843.04	133.25	10/2020 03/2023	03/2023	29	0	
196	KIRANDUL - JAGDALPUR DOUBLING - [N22000318] ECR, CHHATISGARH	12/2012	1,160.00 -	1,160.83	682.29	03/2020 -	03/2023	36	.07	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
197	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 -	1,547.38	346.97	03/2022 -	03/2023	12	0	
198	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 -	3,791.66	1,237.04	03/2009 -	06/2024	183	29.71	
199	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	1,928.07	691.04	06/2021 -	06/2024	36	137.8	
200	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 -	2,361.74	162.82	03/2022 -	03/2025	36	0	
	<u>Eastern Railways</u>									
201	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	157.94	51.75	11/2018 -	03/2021	28	0	
202	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	542.18 -	693.80	443.81	03/2020 -	03/2021	12	27.96	
203	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	1,425.44	637.42	02/2013 -	03/2024	133	134.8	
204	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	1,619.48	868.58	03/2019 12/2009	03/2025	72	36.22	1. Acquisition of land in stretch of 3.126 KM between Kamarpukur and Mayanapur and pending over of 5.679 KM stretch possession to Railway. 2. Villagers of Vill.Bhadadighi, Hooghly District,are not allowing to work over a pond namely .Bhabadighi between Goghat and Kamarpukur . 3. Tarakeswar to Dhaniakhali (19 Km) New line, Arambagh – Irphala (18.3 Km) New line , Irphala – Ghatal (11.2 Km) New line and Arambagh – Champadanga (23.30 Km) New line -- Work could not be started due to non availability of land

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
205	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	1,106.62 -	1,091.59	839.63	12/2010 12/2017	03/2025	171	-1.36	Govt. of West Bengal to deposit Rs. 232.99 Cr. for their balance share towards project Katwa- BWN G.C.
206	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER, MULTI STATE	04/1987	406.99 -	545.70	148.43	03/2006 -	03/2025	228	34.08	Land is required for execution of the MM projects
207	PIRPAINTI-JASIDIH - [N22000219]ER, MULTI STATE	04/2013	915.98 -	2,137.81	294.91	03/2022 -	03/2025	36	133.39	1. Jharkhand & Bihar Government to expedite land acquisition. Milestones may be set only after physical possession of land. 2. Jharkhand Govt. is to deposit Rs. 158.50 Crs. as share of expenditure incurred in this project..
208	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONG WITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER, MULTI STATE	04/2001	923.52 -	995.10	448.78	03/2016 -	03/2025	108	7.75	1 Krishnanagar City (Dhubulia) – Charatala (13.00KM) New line, Krishnanagar – Chapra (19.2 KM) New line Work could not be started due to non – availability of land. 2 For Krishnanagar – Nabadwipghat (12.2 KM) Gauge Conversion— (Section Krishnanagar – Amghata) could not be commissioned due to religious structures in alignment and Amghata to Nabadwipghat work is held up due to 41 nos. of unauthorized crossings.
209	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER, MULTI STATE	04/2005	595.51 -	769.40	102.47	03/2017 -	03/2025	96	29.2	Suri – Prantik New Line (33.90 km). The land acquisition details for 250.627 Hectares, submitted to Govt. of West Bengal.
210	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER, MULTI STATE	04/2010	277.28 -	266.32	160.40	03/2016 -	03/2025	108	-3.95	For Bira - Chakla (11.50) New line- The work will start after acquisition and handing over of land by State Government.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
211	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17	296.43	234.43	03/2017	03/2025	96	-18.82	Baruipara – Furfura (12.30 km) New line - Work could not be started due to non availability of land.
212	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54	494.59	32.00	03/2005	03/2025	240	.01	Budge Budge to Pujali (11.00 km) New Line, Pujali – Uluberia (Birshivpur) (10.25 Km) New Line and Pujali – Bahrahat (9.75 Km) New line-- Work could not be started due to non availability of land
213	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96	680.68	158.60	02/2012	03/2025	157	36.15	Sangrampur – Krishanchandpur (25 Km) New Line, Diamond Harbour (Gurudasnagar) – Bahrahat (21 Km) New Line and Daimond Harbour (Gurudasnagar) - Kulpi (17.25 Km) New Line: Work could not be started due to non availability of land.
214	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42	257.42	106.51	03/2014	03/2025	132	0	226.542 acres of land required to be acquired for the MM work.
215	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60	335.62	1.12	03/2017	03/2026	108	12.02	
	<u>Indian Railway Construction Company Limited</u>									
216	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON,CHHATISGARH	04/2013	3,055.00	3,055.00	1,729.64	09/2018	12/2020	27	0	
217	GEVRA ROAD PENDRA ROAD - [N22000488]IRCON,CHHATISGARH	02/2014	2,288.00	4,970.11	619.50	03/2022	12/2022	9	117.23	
218	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA	04/2016	5,200.00	1,700.43	48.00	03/2020	06/2023	39	-67.3	
	<u>Metropolitan Rapid Transport Projects</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
219	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 1,781.98	2,980.41	1,417.63	03/2004 -	03/2021	204	501.57	
220	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 918.53	918.53	284.75	03/2014 03/2021	03/2021	84	-82.67	
221	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	63	75.91	
	<u>North Central Railway</u>									
222	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	2,912.96 -	3,845.60	137.90	03/2022 -	12/2024	33	32.02	
	<u>North East Frontier Railway</u>									
223	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	297.32 -	614.00	274.97	03/2019 -	03/2020	12	106.51	
224	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	4,454.17 13,809.00	12,524.00	9,123.93	03/2011 -	03/2020	108	181.17	
225	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	385.20 1,532.00	1,532.00	629.19	03/2019 -	03/2020	12	297.72	
226	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 2,145.00	2,145.00	932.80	03/2019 -	03/2020	12	302.54	
227	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	314.00 728.00	728.00	704.09	03/2019 -	03/2020	12	131.85	
228	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	1,180.19 3,300.00	4,541.00	3,279.71	12/2008 -	03/2021	147	284.77	
229	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52 -	4,600.00	781.71	03/2015 -	10/2021	79	97.72	
230	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	569.63 -	650.00	45.24	03/2020 -	12/2021	21	14.11	
231	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	2,393.47 4,968.00	5,021.45	3,075.08	03/2014 03/2022	03/2022	96	109.8	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>North Eastern Railway</u>									
232	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	477.31	328.19	01/2019 -	01/2020	12	61.8	
233	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH	04/2017	622.50 427.00	426.74	179.51	04/2017 -	01/2020	33	-31.45	
234	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	213.35	8.97	04/2016 -	06/2020	50	.16	
235	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	1,028.95	26.06	12/2019 -	04/2021	16	-12.65	
236	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	276.90	-	04/2017 -	04/2022	60	0	
237	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	150.00	-	04/2017 -	10/2022	66	0	
	<u>North Western Railway</u>									
238	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	294.90	141.40	10/2018 -	10/2019	12	24.47	
239	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	303.56	262.32	11/2019 -	05/2020	6	42.26	
240	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 281.03	410.00	351.23	02/2019 -	05/2020	15	69.36	
241	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	348.55	215.47	12/2019 -	06/2020	6	41.64	
242	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	420.18 -	420.18	160.53	03/2020 -	06/2020	3	0	
243	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 780.98	886.41	525.78	02/2019 -	03/2021	25	116.16	
244	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	685.99	47.07	03/2020 -	04/2022	25	14.33	
245	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	808.85	47.07	08/2022 -	09/2022	1	0	
	<u>Northern Railway</u>									
246	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	694.00	220.42	12/2011 -	03/2021	111	141.81	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
247	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 -	845.58	834.59	03/2016 -	03/2021	60	35.29	
248	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	27,949.00	19,403.28	11/2002 -	06/2022	235	1017.96	
249	NANGALDAM-TALWARA(NL), NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	2,010.00	654.07	07/2012 -	03/2024	140	346.67	
	<u>Rail Vikas Nigam Ltd.</u>									
250	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	385.00	386.30	03/2009 03/2009	12/2019	129	188.58	
251	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	1,185.64 -	1,844.47	1,783.59	12/2017 -	03/2020	27	55.57	
252	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	1,200.00	1,147.34	03/2019 -	03/2020	12	29.45	
253	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	1,402.02 -	1,100.00	1,050.36	03/2020 -	06/2020	3	-21.54	
254	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	816.55	686.11	03/2016 -	12/2020	57	29.06	
255	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	948.04 -	1,500.00	1,323.18	03/2020 -	03/2021	12	58.22	
256	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH	04/2011	1,485.85 -	1,485.85	1,074.88	12/2020 -	03/2021	3	0	
257	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70 -	1,202.70	914.39	02/2015 -	12/2021	82	0	
258	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,548.66 -	1,548.66	1,268.31	12/2021 -	03/2022	3	0	
259	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	1,563.45	03/2020 -	03/2022	24	0	
260	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	1,120.00	1,010.21	03/2019 -	06/2022	39	18.78	
261	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	1,183.25	1,072.44	12/2020 -	12/2022	24	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
262	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA	04/2010	2,127.00 -	2,900.00	1,660.87	03/2023 -	03/2024	12	36.34	
263	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60 -	750.56	372.23	03/2022 -	12/2024	33	-20.46	
264	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92 -	1,765.92	601.87	03/2023 -	12/2024	21	0	
265	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	4,259.48	2,237.39	03/2016 -	03/2025	108	7.78	
266	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	2,913.50	849.88	03/2016 -	03/2025	108	0	
267	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00 -	16,216.00	1,655.10	12/2024 -	03/2025	3	0	
268	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,733.86	40.13	03/2014 -	12/2025	141	18.95	
	<u>South Central Railway</u>									
269	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 1.00	1,723.00	1,368.46	03/2000 -	03/2021	252	0	
270	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 -	2,120.16	412.87	03/2009 -	03/2023	168	102.85	
271	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	1,160.48 -	1,160.48	288.38	03/2010 -	03/2023	156	0	
272	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	2,063.03	675.97	03/2021 -	03/2023	24	0	
273	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	3,631.00	407.42	03/2022 -	03/2023	12	0	
274	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 -	2,200.00	252.81	03/2023 -	03/2024	12	18.47	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
275	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	2,288.70 -	2,288.70	667.03	03/2021 -	03/2024	36	0	
276	KADAPA-BANGALORE (NL), KADAPA-PENDIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,132.77 -	2,132.77	331.17	03/2014 -	03/2024	120	0	
	<u>South East Central Railway</u>									
277	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH	04/2010	585.93 737.72	1,300.44	646.30	02/2019 03/2020	06/2020	16	121.94	
278	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	511.86 1,756.92	1,756.92	1,661.79	04/2020 12/2020	12/2020	8	243.24	
279	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATISGARH	04/2015	1,973.00 1,973.66	1,973.66	139.42	03/2021 12/2022	12/2022	21	.03	
280	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA	06/2018	229.00 403.00	860.92	39.69	12/2021 03/2023	03/2023	15	275.95	
	<u>South Eastern Railway</u>									
281	RAJKHARSWAN-CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	377.00	180.95	12/2016 08/2018	12/2019	36	153.41	
282	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 358.68	358.68	258.09	12/2018 12/2018	06/2020	18	38.92	
283	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 1,312.96	1,312.96	549.97	03/2020 -	06/2020	3	35.38	
284	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	1,993.24	384.82	03/2021 -	12/2021	9	15.6	
285	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 -	2,373.00	485.04	03/2003 03/2030	03/2030	324	130.97	
	<u>South Western Railway</u>									
286	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 -	889.52	438.39	03/2017 -	03/2020	36	37.96	
287	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,156.94 -	1,140.93	786.13	03/2020 -	03/2021	12	-1.38	
288	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 -	1,870.41	914.00	03/2019 -	03/2021	24	15.84	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
289	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	986.30 -	986.30	297.70	03/2016 -	12/2023	93	0	
290	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 -	279.54	28.51	03/2016 -	12/2023	93	0	
291	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 -	1,382.78	7.35	03/2002 -	03/2024	264	0	
292	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	832.47	.94	03/2016 -	03/2024	96	0	
293	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 -	2,841.84	113.63	12/2018 -	12/2024	72	0	
	<u>Southern Railway</u>									
294	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	1,800.00	170.47	03/2019 -	12/2019	9	1391.3	
295	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	2,072.50	1,386.59	02/2019 -	02/2020	12	185.98	
296	OMALUR-METTURDAM-DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU	10/2013	187.26 -	231.67	108.34	04/2014 -	03/2020	71	23.72	
297	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	980.00	669.21	03/2020 -	03/2021	12	222.39	
298	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU	02/2015	760.00 -	1,182.31	406.32	03/2020 -	06/2021	15	55.57	
299	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	1,567.00	-	03/2024 -	03/2026	24	0	
	<u>West Central Railway</u>									
300	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH	12/2015	1,763.93 -	1,763.93	624.49	03/2020 -	03/2022	24	0	
301	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH	08/2016	582.13 -	1,247.64	154.63	03/2022 -	09/2022	6	114.32	
302	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	6,093.31	1,835.18	05/2008 -	03/2023	178	2360.35	
303	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	424.60 -	2,909.99	1,926.25	03/2021 -	03/2023	24	585.35	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
304	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH	06/2016	2,478.23 -	2,478.23	367.59	03/2022 -	03/2023	12	0	
	<u>Western Railway</u>									
305	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT	02/1991	551.51 809.07	809.07	616.90	03/2019 03/2020	03/2020	12	46.7	
306	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	829.74 1,215.34	1,310.23	1,394.73	03/2020 03/2021	03/2021	12	57.91	
307	DABHOI-CHANDOD (17.07KM) - GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT	04/2017	691.84 663.29	663.29	166.84	03/2020 03/2021	03/2021	12	-4.13	
308	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH	04/2016	700.00 603.69	603.69	92.30	06/2020 06/2021	06/2021	12	-13.76	
309	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 321.62	321.62	125.76	03/2012 03/2022	03/2022	120	1.06	
310	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 858.56	858.96	534.00	03/2019 03/2022	03/2022	36	167.87	
311	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	1,037.15 1,037.15	1,037.15	992.18	03/2021 03/2022	03/2022	12	0	
312	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	3,503.69 3,860.00	3,860.40	1,676.43	03/2022 03/2023	03/2023	12	10.18	
313	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 1,640.04	1,640.04	682.91	03/2022 03/2023	03/2023	12	0	
	Total		1,80,706.42 -	2,65,634.96	1,17,067.04					
	<u>ROAD TRANSPORT AND HIGHWAYS</u>									
	<u>Ministry Of Road Transport And Highways</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
314	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	164.54	89.14	08/2015 -	09/2019	49	0	
315	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969]MORTH,ANDHRA PRADESH	01/2017	263.45 -	263.45	57.97	09/2017 03/2020	09/2019	24	0	
316	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]MORTH,UTTAR PRADESH	10/2013	445.89 653.00	653.29	464.05	03/2017 -	09/2019	30	46.51	
317	CHIKALI TO KHAMGAON - [N24001012]MORTH,MAHARASHTRA	02/2017	548.03 548.00	548.03	287.00	06/2019 -	10/2019	4	0	
318	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA	08/2013	171.96 172.00	172.00	88.30	06/2016 -	11/2019	41	.02	
319	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]MORTH,ANDHRA PRADESH	02/2017	429.43 -	429.43	203.52	11/2017 03/2020	11/2019	24	0	
320	SAKOLI TO BHANDARA - [N24001118]MORTH,MAHARASHTRA	01/2017	362.96 362.96	362.96	37.83	06/2019 -	11/2019	5	0	
321	NASHIK TO PETH - [N24001121]MORTH,MAHARASHTRA	12/2015	289.60 -	289.60	118.81	11/2018 -	11/2019	12	0	
322	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA	03/2014	191.50 192.00	192.00	136.19	05/2016 -	12/2019	43	.26	
323	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MORTH,UTTARAKHAND	06/2017	282.08 -	282.08	77.05	06/2019 -	12/2019	6	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
324	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]MORTH,ANDHRA PRADESH	10/2015	333.21 -	355.89	265.48	12/2015 12/2019	12/2019	48	6.81	
325	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929]MORTH,ANDHRA PRADESH	09/2016	372.68 -	372.68	183.25	02/2017 12/2019	12/2019	34	0	
326	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964]MORTH,ANDHRA PRADESH	08/2016	350.61 -	350.61	303.82	01/2017 12/2019	12/2019	35	0	
327	KHAMGAON TO SHEGAON - [N24001009]MORTH,MAHARASHTRA	02/2017	203.21 203.00	203.21	102.79	05/2019 -	12/2019	7	0	
328	SHEGAON TO DEORI PHATA - [N24001010]MORTH,MAHARASHTRA	02/2017	373.10 373.00	373.10	123.43	05/2019 -	12/2019	7	0	
329	NANDGAON TO MORSHI - [N24001014]MORTH,MAHARASHTRA	01/2017	385.87 386.00	385.87	203.75	06/2019 -	12/2019	6	0	
330	MORSHI TO ACHALPUR - [N24001015]MORTH,MAHARASHTRA	01/2017	341.16 341.00	341.16	153.29	06/2019 -	12/2019	6	0	
331	NAGAJ TO VAJJAPUR - [N24001023]MORTH,MAHARASHTRA	01/2017	376.72 377.00	376.72	168.81	06/2019 -	12/2019	6	0	
332	INDAPUR TO AGARDANDA - [N24001025]MORTH,MAHARASHTRA	01/2017	355.17 355.17	355.17	164.87	07/2019 -	12/2019	5	0	
333	TAKARKHED TO JALNA - [N24001085]MORTH,MAHARASHTRA	09/2017	417.90 418.00	417.90	87.26	06/2019 -	12/2019	6	0	
334	NAIGAONBANDI TO MANGRULPIR - [N24001094]MORTH,MAHARASHTRA	12/2017	244.04 244.00	244.04	25.94	03/2019 -	12/2019	9	0	
335	TALEGAON TO GONAPUR - [N24001096]MORTH,MAHARASHTRA	01/2018	264.41 264.00	264.41	32.71	03/2019 -	12/2019	9	0	
336	PEN TO KHOPOLI - [N24001106]MORTH,MAHARASHTRA	03/2018	301.39 302.00	301.39	-	03/2018 -	12/2019	21	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
337	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MORTH,UTTARAKHAND	08/2016	234.88 -	208.89	118.26	12/2017 -	12/2019	24	-11.07	
338	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO - [N24000930]MORTH,ANDHRA PRADESH	11/2016	378.24 -	378.24	248.70	01/2018 01/2020	01/2020	24	0	
339	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938]MORTH,ANDHRA PRADESH	03/2018	297.12 294.00	294.12	189.72	07/2018 01/2020	01/2020	18	-1.01	
340	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]MORTH,ANDHRA PRADESH	01/2017	576.48 -	576.48	207.93	01/2018 03/2020	01/2020	24	0	
341	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU - [N24000936]MORTH,ANDHRA PRADESH	03/2018	244.95 245.00	244.95	116.71	08/2018 02/2020	02/2020	18	0	
342	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]MORTH,ANDHRA PRADESH	03/2018	289.67 290.00	289.67	80.77	08/2018 02/2020	02/2020	18	0	
343	AKKALKOT TO DHUDHNI - [N24001120]MORTH,MAHARASHTRA	04/2016	211.42 -	211.42	131.85	02/2019 -	02/2020	12	0	
344	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931]MORTH,ANDHRA PRADESH	11/2016	290.15 -	290.15	69.47	05/2017 03/2020	03/2020	34	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
345	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932]MORTH,ANDHRA PRADESH	01/2017	319.28 -	319.28	103.79	08/2017 03/2020	03/2020	31	0	
346	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934]MORTH,ANDHRA PRADESH	03/2018	228.32 -	228.32	34.74	08/2018 03/2020	03/2020	19	0	
347	REHABILITATION AND UPGRADATION OF KARNATAKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]MORTH,ANDHRA PRADESH	03/2016	995.09 995.00	995.09	401.90	05/2016 03/2020	03/2020	46	0	
348	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966]MORTH,ANDHRA PRADESH	01/2016	348.95 -	348.95	161.18	08/2016 03/2020	03/2020	43	0	
349	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967]MORTH,ANDHRA PRADESH	03/2016	444.84 -	444.84	234.31	09/2016 03/2020	03/2020	42	0	
350	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]MORTH,ANDHRA PRADESH	11/2016	376.25 -	376.25	196.09	08/2017 03/2020	03/2020	31	0	
351	INDAPUR TO VADPALE - [N24001114]MORTH,MAHARASHTRA	01/2017	1,202.52 1,202.52	1,202.52	635.90	12/2019 -	03/2020	3	0	
352	VADPALE TO BHOGAN KHURD - [N24001115]MORTH,MAHARASHTRA	01/2017	1,598.47 1,598.47	1,598.47	751.91	11/2019 -	03/2020	4	0	
353	KOLHA TO NASRATPUR - [N24001111]MORTH,MAHARASHTRA	04/2016	281.78 282.00	281.78	47.73	04/2019 -	04/2020	12	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
354	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]MORTH,ANDHRA PRADESH	03/2018	504.19 504.00	504.19	201.11	11/2018 05/2020	05/2020	18	0	
355	WAKAN PALI KHOPOLI - [N24001026]MORTH,MAHARASHTRA	01/2017	376.19 376.19	376.19	29.03	05/2019 -	05/2020	12	0	
356	DEORI TO AMGAON - [N24001032]MORTH,MAHARASHTRA	01/2017	409.62 410.00	409.62	171.78	05/2019 -	05/2020	12	0	
357	DIGRAS DARWAH KARANJA - [N24001013]MORTH,MAHARASHTRA	01/2017	391.06 391.00	391.06	68.00	06/2019 -	06/2020	12	0	
358	KARAD TO TAGAON - [N24001053]MORTH,MAHARASHTRA	01/2017	537.81 538.00	537.81	85.97	06/2019 -	06/2020	12	0	
359	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MORTH,MAHARASHTRA	02/2017	407.19 407.00	407.19	25.00	06/2019 -	06/2020	12	0	
360	MALEWADA TO CHIMUR - [N24001104]MORTH,MAHARASHTRA	10/2016	322.55 -	322.55	156.91	06/2019 -	06/2020	12	0	
361	PARLI PIMPLA DAHIGUDA - [N24001138]MORTH,MAHARASHTRA	02/2017	205.72 205.72	205.72	30.42	06/2019 -	06/2020	12	0	
362	MANGAON TO DIGHI PORT - [N24001024]MORTH,MAHARASHTRA	01/2017	457.52 457.52	457.52	202.98	07/2019 -	07/2020	12	0	
363	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963]MORTH,ANDHRA PRADESH	01/2018	418.03 -	418.03	144.09	08/2018 08/2020	08/2020	24	0	
364	WADI TO ASOLA - [N24001022]MORTH,MAHARASHTRA	01/2017	363.82 363.82	363.82	41.10	09/2019 -	09/2020	12	0	
365	BARASGAON TO RAHATEE - [N24001113]MORTH,MAHARASHTRA	07/2016	289.11 290.00	289.11	148.00	09/2018 -	04/2021	31	0	
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
366	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL, ARUNACHAL PRADESH	04/2016	198.00 -	198.00	155.94	10/2016 -	10/2019	36	0	
367	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL, TRIPURA	10/2014	369.00 -	369.00	308.97	03/2018 12/2019	12/2019	21	0	
368	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8 - [N24001184]NHIDCL, DELHI	07/2017	269.69 -	269.69	-	09/2019 -	12/2019	3	0	
369	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL, ARUNACHAL PRADESH	12/2016	138.93 155.00	155.00	72.97	01/2017 -	01/2020	36	11.57	
370	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL, ARUNACHAL PRADESH	03/2015	394.00 -	394.00	272.92	06/2018 -	03/2020	21	0	
371	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL, NAGALAND	03/2016	396.52 339.55	396.52	234.03	08/2016 -	06/2020	46	0	
372	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL, ASSAM	05/2015	454.89 -	454.89	123.20	05/2018 05/2020	12/2020	31	0	
373	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL, ARUNACHAL PRADESH	02/2017	168.32 168.32	168.32	33.51	04/2017 02/2018	02/2021	46	0	
374	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL, ARUNACHAL PRADESH	02/2017	180.57 180.57	180.57	13.73	04/2017 02/2018	02/2021	46	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
375	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH	02/2017	216.71 216.71	216.71	16.40	04/2017 02/2018	02/2021	46	0	
376	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH	02/2017	167.28 167.28	167.28	18.94	04/2017 02/2018	02/2021	46	0	
377	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH	03/2017	284.09 284.09	284.09	76.20	04/2017 03/2018	03/2021	47	0	
378	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM	01/2016	294.17 -	294.17	63.00	01/2016 02/2019	04/2021	63	0	
379	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL,MANIPUR	08/2017	517.57 -	457.77	137.04	10/2018 -	10/2021	36	-11.55	
380	4 LANING OF JORHAT TO JHANJHI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM	06/2015	437.39 -	437.39	9.30	06/2018 12/2020	12/2021	42	0	
381	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM	06/2015	463.49 -	463.49	22.32	06/2018 01/2021	12/2021	42	0	
382	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM	01/2016	252.00 -	252.00	4.74	01/2016 12/2021	12/2021	71	0	
383	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH	01/2017	1,253.10 -	1,253.10	158.90	03/2017 -	03/2022	60	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>National Highways Authority Of India</u>									
384	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 1,544.00	1,544.00	1,446.45	09/2016 -	09/2019	36	21.9	NIL
385	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 507.70	507.70	495.63	06/2016 -	09/2019	39	-15.8	
386	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 1,240.03	1,057.60	1,000.89	06/2019 12/2016	09/2019	3	-2.22	
387	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGPUR - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	637.18	588.00	06/2019 -	09/2019	3	0	
388	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	649.00	296.30	06/2019 -	09/2019	3	0	
389	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 767.03	767.03	555.72	08/2018 -	09/2019	13	0	
390	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	328.47	06/2008 -	10/2019	136	0	
391	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	3,220.15	05/2014 -	10/2019	65	0	
392	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	425.19	276.40	09/2016 09/2014	10/2019	37	0	
393	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 537.16	537.16	500.61	07/2018 -	10/2019	15	-6.46	
394	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	972.50	1,492.00	07/2017 -	10/2019	27	0	
395	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	596.67	392.06	05/2018 10/2019	10/2019	17	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
396	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	479.20	711.38	05/2018 03/2018	10/2019	17	0	
397	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	399.54	195.59	04/2019 -	10/2019	6	0	
398	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	2,982.00	276.87	04/2019 10/2019	10/2019	6	87.84	
399	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN	08/2016	320.30 -	320.30	237.81	01/2019 -	10/2019	9	0	
400	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN	06/2016	763.23 -	763.23	216.17	06/2019 -	11/2019	5	0	
401	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	2,016.00	1,996.00	04/2019 11/2019	11/2019	7	0	
402	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH	06/2017	648.33 -	306.00	151.65	06/2017 -	11/2019	29	-52.8	
403	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	232.49	-	10/2017 -	11/2019	25	0	
404	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	946.00	818.53	06/2018 -	12/2019	18	0	
405	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	943.17	08/2012 -	12/2019	88	0	
406	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	2,387.46	03/2013 -	12/2019	81	0	
407	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,159.10	03/2014 -	12/2019	69	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
408	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	1,364.18	03/2013 -	12/2019	81	0	
409	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,173.80	08/2013 -	12/2019	76	0	
410	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	1,396.18	2,894.94	09/2014 -	12/2019	63	0	
411	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI, RAJASTHAN	11/2012	530.07 -	530.07	556.02	08/2016 -	12/2019	40	0	
412	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL	12/2015	1,083.00 -	1,083.00	26.64	06/2018 -	12/2019	18	0	
413	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI, TELANGANA	12/2015	1,423.96 897.03	897.03	737.19	11/2018 07/2019	12/2019	13	-37	
414	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI, PUNJAB	10/2015	447.29 746.43	746.43	600.33	12/2017 06/2020	12/2019	24	66.88	
415	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI, MAHARASHTRA	07/2015	1,871.34 67.34	1,871.34	3,495.79	01/2018 12/2018	12/2019	23	0	
416	CONSTRUCTION OF ROB – FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI, WEST BENGAL	03/2016	229.37 -	229.37	78.31	11/2018 -	12/2019	13	0	
417	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI, HARYANA	08/2016	248.97 -	248.97	240.44	05/2019 -	12/2019	7	0	TBRL Issue: 23.4875 Acres land is not available due to transfer of TBRL land in favour of NHAI. Letter written by NHAI HQ in Apr 2019 to MoRTH to take-up the case with MoD for waiver of land compensation of Rs 31 Cr and to hand over the possession of land. The proposal is pending with MoRTH/MOD.
418	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI, MAHARASHTRA	01/2017	244.90 -	244.90	243.33	05/2019 -	12/2019	7	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
419	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	244.27	141.45	09/2017 -	12/2019	27	0	
420	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	597.00	587.64	10/2017 04/2018	01/2020	27	0	
421	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	323.72	252.99	08/2018 -	01/2020	17	0	
422	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	639.97	274.24	10/2017 -	01/2020	27	0	
423	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	478.00	315.11	10/2013 -	02/2020	76	-11	
424	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	722.46	722.46	07/2018 12/2019	02/2020	19	19.25	
425	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	230.00	337.76	04/2008 -	03/2020	143	10.58	
426	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	470.01	05/2010 -	03/2020	118	0	
427	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 2,967.50	2,967.50	3,986.72	11/2011 -	03/2020	100	167.82	
428	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 1,302.98	934.46	531.34	03/2018 -	03/2020	24	0	
429	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	1,388.00	1,153.07	08/2018 -	03/2020	19	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
430	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI, CHHATISGARH	12/2015	726.67 598.13	598.13	414.73	04/2018 03/2020	03/2020	23	-17.69	The CALA, Raipur had submitted proposal of additional 3A area for 12.6814 Ha (missing Khasra/plot no.) . 3A notification was published in Gazette on 04.07.2018 but CALA, Raipur did not provide revenue/ Khasra map to NHAI inspite of repeated request. In 680m length work was held up due to non-payment of land compensation to land owners, so NHAI has processed the 3D notification for 2.561Ha private land considering urgency at project site without revenue khasra map plan and balance 3D for area 10.1204 Ha was kept in hold due to non-receipt of Revenue Khasra map plan from CALA, Raipur. 3D of 2.561 Ha. land was published on 24.08.2018 . Inspite of repeated request to CALA, Raipur has not submitted revenue Khasra map plan showing 12.6814Ha land so the 3A notification dated 04.07.2018 balance area 10.1204Ha has lapsed on 03.07.2019. Some land owners (which land 3A was published on 04.07.2018 but 3D not published due to want of revenue Khasra map plan) have filed writ petition in Bilaspur High Court and Court passed order that land compensation should be paid to land owners within 09 months from the date of order after duly verification of land proposed in the acquisition. The land acquisition map showing RoW width for 25 villages are still not submitted by SDM Raipur & SDM Simga due to which 3A for balance 10.1204Ha of land could not be processed.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
431	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI, TAMIL NADU	02/2016	707.82 -	707.82	343.21	08/2018 -	03/2020	19	0	
432	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI, UTTAR PRADESH	06/2016	667.00 2,257.49	667.00	464.05	07/2018 -	04/2020	21	0	
433	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI, UTTAR PRADESH	12/2015	667.00 3,007.86	667.00	549.07	06/2018 -	04/2020	22	0	
434	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI, BIHAR	08/2015	322.09 -	322.09	77.53	04/2018 -	04/2020	24	0	
435	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI, KERALA	04/2016	804.97 -	804.97	438.27	06/2018 -	04/2020	22	0	
436	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI, PUNJAB	03/2017	754.54 -	756.27	159.58	03/2020 -	04/2020	1	.23	
437	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI, MAHARASHTRA	09/2015	414.51 -	414.00	531.36	05/2018 03/2019	05/2020	24	-12	
438	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI, MAHARASHTRA	06/2014	923.04 -	923.04	755.97	11/2016 -	05/2020	42	0	
439	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI, TAMIL NADU	02/2016	641.17 -	641.17	354.03	07/2018 -	05/2020	22	0	
440	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI, MAHARASHTRA	02/2017	904.16 911.07	904.16	817.58	02/2020 11/2017	05/2020	3	0	
441	4-LANNING OF WARDHA-BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI, MAHARASHTRA	03/2017	1,030.44 -	1,065.51	1,027.16	03/2020 -	05/2020	2	3.4	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
442	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 2,602.09	1,989.00	852.57	03/2020 11/2017	05/2020	2	0	
443	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	1,187.10	778.87	03/2020 -	05/2020	2	13.97	
444	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	641.17	354.03	07/2016 -	05/2020	46	0	
445	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,333.68	12/2013 -	06/2020	78	0	
446	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,775.04	08/2013 -	06/2020	82	0	
447	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	733.33	07/2014 -	06/2020	71	0	
448	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 41.54	636.24	438.73	05/2018 06/2020	06/2020	25	7.24	
449	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 2,182.03	815.28	520.89	06/2018 -	06/2020	24	0	
450	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 2,433.38	1,027.53	601.13	06/2018 -	06/2020	24	0	
451	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	1,434.00	645.75	03/2020 -	06/2020	3	44.39	
452	4-LANNING OF THALSERRY - MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	1,232.76	278.60	09/2017 -	06/2020	33	9.67	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
453	FOUR LANE OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 2,273.00	2,136.97	1,214.48	12/2018 12/2019	07/2020	19	0	
454	FOUR LANE OF RAMPUR-KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	899.00	532.53	04/2019 07/2020	07/2020	15	0	
455	SIX LANE OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	1,177.00	586.20	03/2020 -	07/2020	4	41.54	
456	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	174.34	224.28	03/2008 -	08/2020	149	-28.84	
457	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	423.83	12/2009 -	08/2020	128	0	
458	DEVELOPMENT OF ADEQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	329.92	06/2013 01/2019	08/2020	86	0	
459	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 870.00	870.00	254.96	03/2019 03/2017	08/2020	17	-25.48	Nil
460	FOUR LANE OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	1,310.00	563.15	03/2020 -	08/2020	5	10.58	
461	4-LANE OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	1,043.28	1,094.73	03/2020 -	08/2020	5	5.56	
462	4-LANE OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	1,160.64	1,082.97	03/2020 -	08/2020	5	5.7	
463	4-LANE OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT	06/2017	1,958.88 -	1,958.88	1,116.85	06/2020 -	08/2020	2	0	
464	4-LANE OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	1,227.87	225.96	09/2017 -	08/2020	35	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
465	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	2,700.65	07/2015 12/2019	09/2020	62	0	
466	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	2,880.38	06/2014 09/2017	09/2020	75	0	
467	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	727.00	421.65	05/2018 -	09/2020	28	36.88	
468	6/8 LANNING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	504.00	220.70	05/2018 04/2019	09/2020	28	-2	
469	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	1,176.37	155.12	08/2017 -	09/2020	37	0	
470	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	701.40	29.48	03/2019 -	11/2020	20	0	
471	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	870.00	36.30	03/2019 -	11/2020	20	0	
472	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	1,373.28	571.96	03/2020 -	11/2020	8	0	
473	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 1,071.00	1,071.00	549.63	03/2017 05/2018	11/2020	44	1.06	
474	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	964.17	370.32	10/2017 -	11/2020	37	0	
475	4-LANNING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	1,655.01	1,867.51	08/2016 -	12/2020	52	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
476	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	2,168.66	621.26	06/2019 -	12/2020	18	0	
477	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	546.00	269.67	07/2019 12/2020	12/2020	17	0	
478	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	591.66	310.56	07/2019 12/2020	12/2020	17	0	
479	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 1,008.00	1,108.00	1,354.09	08/2019 -	12/2020	16	16.55	
480	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	990.61	17.41	09/2017 -	01/2021	40	0	
481	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	400.25	64.89	03/2019 -	02/2021	23	0	
482	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	2,510.04	252.10	08/2019 -	03/2021	19	0	
483	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHATTI - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	446.17	38.97	03/2019 -	03/2021	24	0	
484	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	1,420.00	365.00	03/2020 -	03/2021	12	10.24	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
485	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	649.50	134.58	03/2019 04/2021	04/2021	25	0	
486	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH	03/2018	1,532.62 2,499.00	2,499.00	569.15	03/2021 -	04/2021	1	63.05	
487	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	227.77	-	03/2020 -	05/2021	14	-3.27	
488	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	476.56	-	07/2017 11/2020	06/2021	47	0	
489	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	2,485.93	704.29	06/2020 -	09/2021	15	0	
490	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	950.64	102.51	08/2017 -	02/2022	54	0	
	<u>National Highways Development Project</u>									
491	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH	10/2013	445.89 -	653.29	464.05	03/2017 -	09/2019	30	46.51	
492	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	410.72 -	410.72	216.14	04/2015 -	10/2019	54	0	
493	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH	11/2013	497.05 -	881.05	544.84	05/2017 -	05/2020	36	77.26	
	<u>Public Works Dept Of State</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
494	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA	03/2015	153.21 -	153.21	100.10	01/2017 -	09/2019	32	0	
495	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA	12/2011	159.39 -	159.39	210.29	11/2017 -	09/2019	22	0	
496	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]PWD,HARYANA	01/2017	247.25 -	247.25	144.71	03/2019 03/2020	09/2019	6	0	
497	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO - [N24001143]PWD,UTTAR PRADESH	10/2016	176.94 177.00	176.94	132.45	10/2018 -	09/2019	11	0	
498	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH - [N24001145]PWD,UTTAR PRADESH	05/2013	164.54 165.00	164.54	89.14	08/2015 -	09/2019	49	0	
499	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH	03/2015	271.45 -	271.45	152.90	10/2015 11/2019	11/2019	49	0	
500	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]PWD,WEST BENGAL	03/2016	271.17 291.20	291.20	80.26	11/2018 11/2019	11/2019	12	7.39	
501	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]PWD,MADHYA PRADESH	11/2017	235.91 -	235.91	117.24	02/2018 -	11/2019	21	0	
502	UPGRADATION OF PACHORE-SHUJALPUR ROAD TO 2L + PS - [N24000881]PWD,MADHYA PRADESH	11/2017	184.62 -	184.62	55.27	02/2018 -	11/2019	21	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
503	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]PWD,MADHYA PRADESH	03/2018	214.69 -	214.69	23.06	03/2018 -	11/2019	20	0	
504	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]PWD,MADHYA PRADESH	03/2018	233.04 -	233.04	95.28	03/2018 -	11/2019	20	0	
505	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]PWD,MADHYA PRADESH	11/2017	254.17 -	254.17	139.86	02/2018 -	11/2019	21	0	
506	REHABILITATION AND UPGRADATION TO 2LPS 81 TO 175 - [N24000895]PWD,MADHYA PRADESH	09/2016	287.34 -	287.34	148.65	01/2019 -	11/2019	10	0	
507	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]PWD,MADHYA PRADESH	03/2016	877.79 -	877.79	436.12	06/2019 -	11/2019	5	0	
508	REHABILITATION AND UPGRADATION OF TULSIPUR - BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]PWD,UTTAR PRADESH	03/2016	249.50 -	249.50	150.70	05/2019 -	11/2019	6	0	
509	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]PWD,MADHYA PRADESH	11/2017	392.33 -	392.33	242.88	03/2018 -	11/2019	20	0	
510	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA	01/2014	255.75 348.00	348.43	290.12	09/2017 -	12/2019	27	36.24	
511	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	992.67	853.82	03/2011 -	12/2019	105	58.98	
512	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	327.92	254.24	10/2010 -	12/2019	110	69.3	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
513	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 240.58	151.59	196.76	08/2013 -	12/2019	76	0	
514	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 269.14	269.14	185.49	02/2013 09/2017	12/2019	82	47.65	
515	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	191.08	99.98	08/2015 -	12/2019	52	0	
516	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]PWD,MADHYA PRADESH	03/2018	162.56 -	162.56	88.47	03/2018 -	12/2019	21	0	
517	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]PWD,TELANGANA	10/2016	298.32 -	298.32	77.44	02/2019 -	12/2019	10	0	
518	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]PWD,TELANGANA	10/2016	248.83 -	248.83	88.85	03/2019 -	12/2019	9	0	
519	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]PWD,TELANGANA	01/2017	300.00 -	300.00	99.46	05/2019 -	12/2019	7	0	
520	REHABILITATION AND UPGRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL - MALLAMPALLY SECTION OF NH-365 - [N24000997]PWD,TELANGANA	03/2018	192.67 -	192.67	107.37	07/2019 -	12/2019	5	0	
521	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM - [N24001153]PWD,ASSAM	11/2010	197.37 -	197.37	88.86	02/2014 -	12/2019	70	0	
522	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]PWD,MIZORAM	08/2010	186.96 -	305.61	275.06	09/2014 -	12/2019	63	63.46	
523	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]PWD,MADHYA PRADESH	11/2017	249.05 -	249.05	118.29	07/2018 -	01/2020	18	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
524	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH	03/2015	511.83 -	511.83	240.05	08/2017 -	02/2020	30	0	
525	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]PWD,MADHYA PRADESH	01/2016	809.16 -	809.16	219.42	07/2018 -	02/2020	19	0	
526	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	954.43 -	954.43	235.61	09/2015 -	03/2020	54	0	
527	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]PWD,MADHYA PRADESH	02/2018	279.44 -	279.44	76.00	03/2018 -	04/2020	25	0	
528	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]PWD,MADHYA PRADESH	01/2017	373.82 -	373.82	116.34	09/2019 -	05/2020	8	0	
529	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]PWD,KARNATAKA	05/2018	171.60 -	171.60	.86	05/2018 -	05/2020	24	0	
530	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	377.99	305.38	10/2010 -	06/2020	116	93.8	
531	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]PWD,MADHYA PRADESH	03/2018	166.21 -	166.21	30.52	08/2018 -	06/2020	22	0	
532	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]PWD,MADHYA PRADESH	01/2017	205.05 -	205.05	73.22	03/2017 -	06/2020	39	0	
533	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]PWD,MADHYA PRADESH	03/2018	217.22 -	217.22	20.43	08/2018 -	06/2020	22	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
534	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]PWD,MADHYA PRADESH	02/2018	169.63 -	169.63	9.35	03/2018 -	07/2020	28	0	
535	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]PWD,BIHAR	05/2014	199.98 -	199.98	153.43	08/2016 -	12/2020	52	0	
536	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION - [N24001173]PWD,KARNATAKA	02/2017	157.32 188.00	157.32	-	05/2019 -	05/2021	24	0	
537	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]PWD,WEST BENGAL	03/2016	160.27 213.97	213.97	20.11	08/2019 -	08/2021	24	33.51	
538	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]PWD,WEST BENGAL	06/2016	236.78 263.26	263.26	59.92	08/2019 -	08/2021	24	11.18	
	Total		1,39,959.97 -	1,47,056.07	95,434.88					
	<u>TELECOMMUNICATIONS</u>									
	<u>Bharat Sanchar Nigam Limited</u>									
539	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]BSNL,MAHARASHTRA	01/2018	231.80 240.10	240.10	117.63	10/2018 12/2019	12/2019	14	3.58	
	<u>Department Of Telecommunication</u>									
540	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	24,664.00	8,397.00	07/2015 -	05/2020	58	84.97	
	Total		13,565.80 -	24,904.10	8,514.63					
	<u>URBAN DEVELOPMENT</u>									
	<u>Ahmedabad Metro Rail</u>									
541	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT	11/2014	10,773.00 -	10,773.00	6,057.03	12/2018 -	07/2020	19	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>Bangalore Metro Rail Corporation Limited</u>									
542	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	26,405.14	499.85	02/2019 -	03/2020	13	0	
	<u>Central Public Works Department</u>									
543	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	156.13	08/2016 -	10/2019	38	0	
544	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	199.91	11/2014 -	10/2019	59	0	
545	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB	02/2014	388.00 -	488.28	437.01	05/2017 -	10/2019	29	25.85	
546	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	266.00	-	12/2013 -	10/2019	70	132.8	
547	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]CPWD,PUNJAB	08/2016	294.00 -	294.00	203.32	04/2019 -	02/2020	10	0	
548	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN	12/2016	549.31 559.47	559.47	348.69	07/2019 12/2019	02/2020	7	1.85	
549	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	165.23	92.05	10/2012 -	03/2020	89	0	
550	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD,TAMIL NADU	12/2015	209.00 -	209.00	130.62	10/2019 -	03/2020	5	0	
551	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	85.33	03/2016 -	09/2020	54	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
552	RESIDENTIAL QUATERS FOR HAL, BANGLORE - [N28000103]CPWD, KARNATAKA	12/2016	246.31 -	246.31	72.38	02/2020 -	09/2020	7	0	
553	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]CPWD, MAHARASHTRA	01/2018	223.37 -	223.37	33.01	07/2020 09/2020	09/2020	2	0	
554	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD, MANIPUR	02/2014	216.69 -	216.69	52.00	03/2015 -	10/2020	67	0	
555	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD, BIHAR	02/2016	496.18 496.00	498.99	92.22	06/2017 -	10/2020	40	.57	
556	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD, DELHI	06/2015	197.33 -	197.33	48.86	04/2019 -	11/2020	19	0	
557	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB - [N28000120]CPWD, PUNJAB	01/2018	430.00 -	430.00	77.69	05/2020 -	01/2021	8	0	
558	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD, DELHI	10/2013	1,219.21 -	2,000.00	374.71	10/2019 -	03/2021	17	64.04	
559	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD, TELANGANA	10/2016	209.84 -	209.84	35.79	03/2020 -	05/2021	14	0	
	<u>Hindustan Steelwork Construction Limited</u>									
560	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL, BIHAR	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72	0	
	<u>Kochi Metro Rail Corporation Ltd</u>									
561	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL, KERALA	07/2012	5,181.79 -	5,687.79	5,188.00	07/2017 -	12/2019	29	9.76	
	<u>Maharashtra Metro Rail Corporation Ltd.</u>									
562	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC, MAHARASHTRA	12/2016	11,420.00 -	11,420.00	2,896.26	11/2021 01/2022	01/2022	2	0	
	<u>Mumbai Metro Rail Corporation Ltd</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (September 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
563	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL, MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	05/2020	64	0	
	<u>Nagpur Metro Rail Corporation Ltd</u>									
564	NAGPUR METRO RAIL - [N28000085]NMRCL, MAHARASHTRA	08/2014	8,680.00 -	8,680.00	6,237.34	03/2018 -	12/2019	21	0	
	Total		92,109.92 -	93,661.70	23,969.41					
	<u>WATER RESOURCES</u>									
	<u>Polavaram Project Authority</u>									
565	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA, ANDHRA PRADESH	02/2009	10,151.04 -	55,548.87	16,417.99	03/2020 -	06/2021	15	447.22	
	Total		10,151.04 -	55,548.87	16,417.99					
	Grand Total		8,45,560.27	10,81,723.56	5,64,991.94					

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Annexure - VII

(September 2019)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
	<u>Bhavini Limited</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,840.00	09/2010 -	10/2021	95.88	133
	<u>Nuclear Power Corporation Of India Limited</u>							
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	12/2015 -	06/2020	44.69	54
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]	10/2009	12,320.00 -	17,079.00	12/2016 -	12/2020	38.63	48
	Total		27,271.00 -	40,499.00				
	<u>CIVIL AVIATION</u>							
	<u>Airport Authority Of India Limited</u>							
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]	09/2015	338.93 -	339.00	06/2019 -	12/2019	.02	6
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28	21
	Total		653.54 -	780.33				
	<u>COAL</u>							
	<u>Neyveli Lignite Corporation</u>							
6	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	06/2011	5,907.11 -	7,080.41	12/2015 -	12/2019	19.86	48
	<u>Singareni Colliers Company Limited</u>							
7	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	03/2015 -	03/2021	114.60	72
8	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	03/2019 -	03/2020	11.42	12
9	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	03/2012 -	03/2024	80.24	144
10	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 -	473.22	03/2015 -	03/2021	5.85	72
11	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86	132
	<u>South-Eastern Coal Fields Limited</u>							
12	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	03/2015 -	03/2020	201.44	60
	<u>Western Coal Fields Limited</u>							

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(September 2019)

Date of Commissioning (Month/Year)								
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
13	KAMPTEE DEEP OC MINE - [N06000141	11/2015	277.65 -	313.34	03/2021 -	03/2024	12.85	36
14	ADASA UG TO OC - [N06000133	08/2015	288.90 -	333.43	03/2023 -	03/2024	15.41	12
	Total		8,301.00 -	10,390.07				
	<u>FERTILISERS</u>							
	<u>Rashtriya Chemical & Fertiliser Limited</u>							
15	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY [N08000009	10/2014	197.79 -	209.44	11/2016 -	09/2019	5.89	34
	Total		197.79 -	209.44				
	<u>HEALTH AND FAMILY WELFARE</u>							
	<u>Hospital Services Consultancy Corporation Ltd</u>							
16	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003	02/2013	414.11 -	513.89	11/2013 -	10/2020	24.10	83
	Total		414.11 -	513.89				
	<u>PETROLEUM</u>							
	<u>Bharat Petroleum Corporation Limited</u>							
17	HALDIA LPG IMPORT FACILITY - [N16000223	03/2015	694.00 -	1,097.54	10/2018 -	12/2019	58.15	14
18	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314	12/2015	1,112.00 -	1,507.24	06/2019 -	02/2022	35.54	32
19	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227	11/2014	4,588.29 -	5,245.96	08/2018 -	11/2019	14.33	15
	<u>Gas Authority Of India Limited</u>							
20	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II [N16000285	06/2009	2,915.00 2,915.00	3,049.47	12/2012 -	02/2022	4.61	110
	<u>Indian Oil Corporation Limited</u>							
21	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253	05/2016	4,497.00 -	6,025.00	12/2018 -	02/2021	33.98	26
	<u>Mangalore Refinery And Petrochemicals Limited</u>							
22	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE [N16000256	10/2015	135.00 171.00	170.70	03/2019 -	10/2019	26.44	7
23	SEA WATER DESALINATION PLANT - [N16000319	11/2017	581.00 -	621.00	03/2020 -	09/2020	6.88	6
	<u>Oil & Natural Gas Corporation Limited</u>							

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(September 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
24	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]	06/2010	202.94 -	345.92	01/2014 -	11/2019	70.45	70
25	DEVELOPMENT OF B-147 FIELD - [N16000292]	02/2017	546.15 -	565.15	11/2019 -	03/2020	3.48	4
26	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79 -	1,683.06	05/2013 -	12/2019	95.30	79
27	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	12/2019	29.42	57
28	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	04/2018 -	05/2020	1.77	25
29	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]	02/2019	3,660.71 -	3,740.05	04/2021 -	05/2021	2.17	1
30	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]	02/2017	4,006.83 -	4,475.92	05/2021 -	12/2021	11.71	7
	<u>Oil India Limited</u>							
31	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	438.84	03/2017 -	12/2019	24.47	33
32	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	01/2018	543.91 -	682.90	02/2020 -	06/2020	25.55	4
	Total		29,947.50 -	35,561.59				
	<u>POWER</u>							
	<u>National Hydro-Electric Power Corporation</u>							
33	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	9,997.11	09/2009 -	12/2021	155.06	147
	<u>National Thermal Power Corporation</u>							
34	RAMMAM-III HEPP (3X40 MW) - [N18000178]	09/2014	1,381.84 -	1,592.34	09/2019 -	02/2022	15.23	29
35	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	5,867.38	03/2013 -	01/2021	96.99	94
36	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	9,996.59	07/2012 -	09/2020	86.75	98
37	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]	04/2012	9,750.89 -	12,176.28	02/2017 -	06/2020	24.87	40
38	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	10/2017 -	03/2020	7.55	29
39	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	12,865.92	01/2018 -	03/2020	10.55	26
40	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 -	13,740.53	12/2018 -	09/2020	9.64	21

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(September 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
41	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,164.05	06/2019 -	09/2021	5.55	27
42	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	17,304.00	05/2018 -	03/2021	33.47	34
43	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	21,312.11	10/2011 -	08/2021	145.16	118
	<u>North East Electric Power Corporation</u>							
44	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	7,927.34	12/2009 06/2016	10/2019	217.49	118
	<u>Power Grid Corporation Of India Limited</u>							
45	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03	07/2017 -	10/2019	27.92	27
46	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	546.36	11/2016 -	03/2020	4.61	40
47	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	06/2014 -	10/2019	31.17	64
48	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	04/2016 -	11/2019	38.61	43
49	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT [N18000061]	10/2008	4,824.12 -	5,071.94	10/2012 -	12/2019	5.14	86
50	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,880.36	12/2018 -	12/2020	34.61	24
51	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,072.36	12/2018 -	12/2020	90.82	24
52	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	14,719.10	08/2013 -	03/2022	32.24	103
	<u>Thdc India Limited</u>							
53	DHUKWAN SMALL HYDRO PROJECT - [N18000189]	05/2011	195.42 -	294.60	02/2014 -	12/2019	50.75	70
54	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT [N18000042]	08/2008	2,491.58 -	4,397.80	06/2013 -	12/2022	76.51	114
55	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	5,024.35	02/2016 -	06/2022	203.22	76
	Total		1,30,663.48 -	1,89,481.24				
	<u>RAILWAYS</u>							
	<u>Central Railways</u>							
56	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 -	305.00	03/2019 -	12/2019	65.71	9
57	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89 -	1,377.48	03/2021 -	03/2022	73.73	12

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(September 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
58	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [N220100181]	02/1997	2,271.50 -	3,712.50	03/2021 -	03/2022	63.44	12
	<u>Container Corporation Of India</u>							
59	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 -	235.00	03/2019 -	12/2020	.21	21
	<u>East Central Railways</u>							
60	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	477.88 283.95	751.55	03/2012 -	03/2020	57.27	96
61	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]	04/2009	548.00 -	819.01	03/2020 -	03/2022	49.45	24
62	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR [N220100240]	04/1997	324.73 -	1,050.00	03/2012 -	03/2020	223.35	96
63	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 -	1,185.73	03/2021 -	03/2022	62.06	12
64	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 -	1,215.54	03/2021 -	03/2022	63.37	12
	<u>East Coast Railway</u>							
65	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 -	238.03	03/2020 -	03/2021	52.77	12
66	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	04/2015	701.61 -	810.02	11/2018 -	03/2022	15.45	40
67	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,160.83	03/2020 -	03/2023	.07	36
68	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	1,111.99 -	1,539.28	02/2019 -	03/2022	38.43	37
69	TALCHER-BIMALAGARH(NL)(ECOR) - [N220100328]	04/2005	810.78 -	1,928.07	06/2021 -	06/2024	137.80	36
70	KHURDA ROAD-BOLANGIR(NL)ECOR - [N220100284]	04/1994	2,923.13 -	3,791.66	03/2009 -	06/2024	29.71	183
	<u>Eastern Railways</u>							
71	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY [N22000239]	04/2011	299.60 -	335.62	03/2017 -	03/2026	12.02	108
72	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE- PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]	04/2010	494.54 -	494.59	03/2005 -	03/2025	.01	240
73	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP- BUDAKHALI AND CHANDRANAG - [N22000216]	04/1987	406.99 -	545.70	03/2006 -	03/2025	34.08	228
74	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	499.96 -	680.68	02/2012 -	03/2025	36.15	157
75	HANSDIHA-GODDA NL - [N22000236]	04/2011	542.18 -	693.80	03/2020 -	03/2021	27.96	12

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(September 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
76	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225	04/2005	595.51 -	769.40	03/2017 -	03/2025	29.20	96
77	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224	04/2001	923.52 -	995.10	03/2016 -	03/2025	7.75	108
78	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	607.09 -	1,425.44	02/2013 -	03/2024	134.80	133
79	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	1,188.91 -	1,619.48	03/2019 12/2009	03/2025	36.22	72
80	PIRPAINTI-JASIDIH - [N22000219	04/2013	915.98 -	2,137.81	03/2022 -	03/2025	133.39	36
	<u>Indian Railway Construction Company Limited</u>							
81	GEVRA ROAD PENDRA ROAD - [N22000488	02/2014	2,288.00 -	4,970.11	03/2022 -	12/2022	117.23	9
	<u>Metropolitan Rapid Transport Projects</u>							
82	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	2,980.41	03/2004 -	03/2021	501.57	204
83	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135	03/2013	4,874.58 -	8,574.97	03/2016 -	06/2021	75.91	63
	<u>North Central Railway</u>							
84	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	04/2011	2,912.96 -	3,845.60	03/2022 -	12/2024	32.02	33
	<u>North East Frontier Railway</u>							
85	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135	04/1983	297.32 -	614.00	03/2019 -	03/2020	106.51	12
86	AGARTALA-AKHAURA NL - [N22000195	04/2012	569.63 -	650.00	03/2020 -	12/2021	14.11	21
87	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210	04/2011	314.00 -	728.00	03/2019 -	03/2020	131.85	12
88	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086	09/2006	385.20 -	1,532.00	03/2019 -	03/2020	297.72	12
89	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087	09/2006	532.87 -	2,145.00	03/2019 -	03/2020	302.54	12
90	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	1,180.19 -	4,541.00	12/2008 -	03/2021	284.77	147
91	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124	04/2006	2,326.52 -	4,600.00	03/2015 -	10/2021	97.72	79
92	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	2,393.47 -	5,021.45	03/2014 -	03/2022	109.80	96
93	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	4,454.17 -	12,524.00	03/2011 -	03/2020	181.17	108
	<u>North Eastern Railway</u>							

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(September 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
94	INDARA - DOHRGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	04/2016 -	06/2020	.16	50
95	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	01/2019 -	01/2020	61.80	12
	<u>North Western Railway</u>							
96	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	294.90	10/2018 -	10/2019	24.47	12
97	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	303.56	11/2019 -	05/2020	42.26	6
98	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	348.55	12/2019 -	06/2020	41.64	6
99	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	410.00	02/2019 -	05/2020	69.36	15
100	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	685.99	03/2020 -	04/2022	14.33	25
101	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	886.41	02/2019 -	03/2021	116.16	25
	<u>Northern Railway</u>							
102	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	694.00	12/2011 -	03/2021	141.81	111
103	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 -	845.58	03/2016 -	03/2021	35.29	60
104	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,010.00	07/2012 -	03/2024	346.67	140
105	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	27,949.00	11/2002 -	06/2022	1,017.96	235
	<u>Rail Vikas Nigam Ltd.</u>							
106	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	385.00	03/2009 03/2009	12/2019	188.58	129
107	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2020	29.06	57
108	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 -	1,120.00	03/2019 -	06/2022	18.78	39
109	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,200.00	03/2019 -	03/2020	29.45	12
110	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 -	1,500.00	03/2020 -	03/2021	58.22	12
111	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	1,185.64 -	1,844.47	12/2017 -	03/2020	55.57	27
112	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95	141
113	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 -	2,900.00	03/2023 -	03/2024	36.34	12
114	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2025	7.78	108

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(September 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>South Central Railway</u>							
115	KOTLPALLI-NARASAPUR (NL) (SCR) - [N220100265]	12/2001	1,045.20 -	2,120.16	03/2009 -	03/2023	102.85	168
116	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	04/2012	1,856.95 -	2,200.00	03/2023 -	03/2024	18.47	12
	<u>South East Central Railway</u>							
117	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00 -	860.92	12/2021 -	03/2023	275.95	15
118	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438]	04/2010	585.93 -	1,300.44	02/2019 -	06/2020	121.94	16
119	GONDIA-JABALPUR(GC),(SECR) - [N220100186]	02/1997	511.86 -	1,756.92	04/2020 -	12/2020	243.24	8
120	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	04/2015	1,973.00 -	1,973.66	03/2021 -	12/2022	.03	21
	<u>South Eastern Railway</u>							
121	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	358.68	12/2018 -	06/2020	38.92	18
122	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND [N22000323]	04/2012	148.77 -	377.00	12/2016 -	12/2019	153.41	36
123	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	1,312.96	03/2020 -	06/2020	35.38	3
124	BONDAMUNDA RANCHI DOUBLING - [N22000396]	03/2016	1,724.20 -	1,993.24	03/2021 -	12/2021	15.60	9
125	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL [N22000402]	04/1998	1,027.40 -	2,373.00	03/2003 -	03/2030	130.97	324
	<u>South Western Railway</u>							
126	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78 -	889.52	03/2017 -	03/2020	37.96	36
127	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 -	1,870.41	03/2019 -	03/2021	15.84	24
	<u>Southern Railway</u>							
128	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]	10/2013	187.26 -	231.67	04/2014 -	03/2020	23.72	71
129	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [N220100262]	09/1995	303.98 -	980.00	03/2020 -	03/2021	222.39	12
130	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING [N22000451]	02/2015	760.00 -	1,182.31	03/2020 -	06/2021	55.57	15
131	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70 -	1,800.00	03/2019 -	12/2019	1,391.30	9
132	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI [N22000079]	09/2007	724.69 -	2,072.50	02/2019 -	02/2020	185.98	12

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(September 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>West Central Railway</u>							
133	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13 -	1,247.64	03/2022 -	09/2022	114.32	6
134	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60 -	2,909.99	03/2021 -	03/2023	585.35	24
135	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35	178
	<u>Western Railway</u>							
136	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	03/2022	1.06	120
137	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]	02/1991	551.51 -	809.07	03/2019 -	03/2020	46.70	12
138	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	858.96	03/2019 -	03/2022	167.87	36
139	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	04/2008	829.74 -	1,310.23	03/2020 -	03/2021	57.91	12
140	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	3,503.69 -	3,860.40	03/2022 -	03/2023	10.18	12
	Total		83,601.46 -	1,77,486.48				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>Ministry Of Road Transport And Highways</u>							
141	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]	08/2013	171.96 172.00	172.00	06/2016 -	11/2019	.02	41
142	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]	03/2014	191.50 192.00	192.00	05/2016 -	12/2019	.26	43
143	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]	10/2015	333.21 -	355.89	12/2015 -	12/2019	6.81	48
144	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]	10/2013	445.89 653.00	653.29	03/2017 -	09/2019	46.51	30
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>							
145	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]	12/2016	138.93 155.00	155.00	01/2017 -	01/2020	11.57	36
	<u>National Highways Authority Of India</u>							
146	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 -	230.00	04/2008 -	03/2020	10.58	143
147	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]	10/2015	593.26 -	636.24	05/2018 -	06/2020	7.24	25

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(September 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
148	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]	11/2012	605.84 -	722.46	07/2018 -	02/2020	19.25	19
149	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]	10/2015	531.13 -	727.00	05/2018 -	09/2020	36.88	28
150	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]	10/2015	447.29 -	746.43	12/2017 -	12/2019	66.88	24
151	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	03/2017	754.54 -	756.27	03/2020 -	04/2020	.23	1
152	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	03/2017	988.34 -	1,043.28	03/2020 -	08/2020	5.56	5
153	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	03/2017	1,030.44 -	1,065.51	03/2020 -	05/2020	3.40	2
154	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]	03/2017	1,059.73 -	1,071.00	03/2017 -	11/2020	1.06	44
155	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]	09/2016	950.69 -	1,108.00	08/2019 -	12/2020	16.55	16
156	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]	03/2017	1,098.06 -	1,160.64	03/2020 -	08/2020	5.70	5
157	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]	03/2017	831.58 -	1,177.00	03/2020 -	07/2020	41.54	4
158	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]	03/2017	1,041.62 -	1,187.10	03/2020 -	05/2020	13.97	2
159	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]	09/2017	1,124.11 -	1,232.76	09/2017 -	06/2020	9.67	33
160	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	03/2017	1,184.71 -	1,310.00	03/2020 -	08/2020	10.58	5
161	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]	03/2017	1,288.07 -	1,420.00	03/2020 -	03/2021	10.24	12
162	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]	03/2017	993.16 -	1,434.00	03/2020 -	06/2020	44.39	3
163	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	04/2014	1,266.60 -	1,544.00	09/2016 -	09/2019	21.90	36
164	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]	03/2018	1,532.62 -	2,499.00	03/2021 -	04/2021	63.05	1
165	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,967.50	11/2011 -	03/2020	167.82	100

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(September 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
166	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 TO 208.300 KM [PACKAGE-IV] - [N24000551]	03/2016	1,587.49 -	2,982.00	04/2019 -	10/2019	87.84	6
	<u>National Highways Development Project</u>							
167	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]	10/2013	445.89 -	653.29	03/2017 -	09/2019	46.51	30
168	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]	11/2013	497.05 -	881.05	05/2017 -	05/2020	77.26	36
	<u>Public Works Dept Of State</u>							
169	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND) - [N24000885]	03/2016	160.27 -	213.97	08/2019 -	08/2021	33.51	24
170	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]	06/2016	236.78 -	263.26	08/2019 -	08/2021	11.18	24
171	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]	01/2013	182.28 -	269.14	02/2013 -	12/2019	47.65	82
172	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]	03/2016	271.17 291.20	291.20	11/2018 -	11/2019	7.39	12
173	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]	08/2010	186.96 -	305.61	09/2014 -	12/2019	63.46	63
174	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]	08/2010	193.69 -	327.92	10/2010 -	12/2019	69.30	110
175	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	01/2014	255.75 348.00	348.43	09/2017 -	12/2019	36.24	27
176	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]	08/2010	195.04 -	377.99	10/2010 -	06/2020	93.80	116
177	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]	11/2010	624.41 -	992.67	03/2011 -	12/2019	58.98	105
	Total		24,756.06 -	33,472.90				
	<u>STEEL</u>							
	<u>National Mineral Development Corporation (Nmhc)</u>							
178	NMDC INTEGRATED STEEL PLANT - [N12000086]	01/2010	15,525.00 -	23,140.00	05/2015 -	07/2020	49.05	62
	Total		15,525.00 -	23,140.00				
	<u>TELECOMMUNICATIONS</u>							

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(September 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>Bharat Sanchar Nigam Limited</u>							
179	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]	01/2018	231.80 -	240.10	10/2018 -	12/2019	3.58	14
	<u>Department Of Telecommunication</u>							
180	NETWORK FOR SPECTRUM - [N26000101]	03/2012	13,334.00 -	24,664.00	07/2015 -	05/2020	84.97	58
	Total		13,565.80 -	24,904.10				
	<u>URBAN DEVELOPMENT</u>							
	<u>Central Public Works Department</u>							
181	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]	12/2008	114.26 266.00	266.00	12/2013 -	10/2019	132.80	70
182	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]	02/2014	388.00 -	488.28	05/2017 -	10/2019	25.85	29
183	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	06/2017 -	10/2020	.57	40
184	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]	12/2016	549.31 -	559.47	07/2019 -	02/2020	1.85	7
185	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	2,000.00	10/2019 -	03/2021	64.04	17
	<u>Kochi Metro Rail Corporation Ltd</u>							
186	KOCHI METRO RAIL PROJECT - [N28000081]	07/2012	5,181.79 -	5,687.79	07/2017 -	12/2019	9.77	29
	Total		7,948.75 -	9,500.53				
	<u>WATER RESOURCES</u>							
	<u>Polavaram Project Authority</u>							
187	POLAVARAM IRRIGATION PROJECT - [N30000002]	02/2009	10,151.04 -	55,548.87	03/2020 -	06/2021	447.22	15
	Total		10,151.04 -	55,548.87				
	Grand Total		3,52,996.53	6,01,488.44				

Details of Projects Without Date of Commissioning

Annexure - VIII

Costing Rs. 150 Crore and above				(September 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>COAL</u>				
	<u>Bharat Coking Coal Limited</u>				
1	MURAI DIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	04/2014 -	-
2	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	04/2015 -	-
3	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND	08/2011	988.35 -	04/2017 -	-
	<u>Eastern Coal Fields Limited</u>				
4	RANIGANJ MASTER PLAN - [N06000163]ECL, WEST BENGAL	08/2009	2,661.73 -	08/2019 -	-
	<u>Neyveli Lignite Corporation</u>				
5	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC, TAMIL NADU	04/2013	1,458.17 -	06/2015 -	-
6	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC, RAJASTHAN	03/2015	522.45 -	09/2019 -	-
7	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC, RAJASTHAN	03/2015	513.63 -	12/2019 -	-
	<u>Singareni Colliers Company Limited</u>				
8	KAKATIYA LONGWALL - [N06000048]SCCL, TELANGANA	12/2008	453.63 -	12/2012 -	-
9	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL, TELANGANA	03/2010	181.19 -	03/2012 -	-
	<u>Western Coal Fields Limited</u>				
10	NEW MAJRI UG TO OC - [N06000128]WCL, MAHARASHTRA	05/2015	295.56 -	03/2019 -	-
11	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL, MAHARASHTRA	02/2016	198.68 -	03/2019 -	-
12	BHATADI EXPANSION OC MINE - [N06000150]WCL, MAHARASHTRA	02/2016	304.52 -	03/2019 -	-
13	GAURI DEEP OC - [N06000181]WCL, MAHARASHTRA	10/2016	164.96 -	03/2019 -	-
	Total		9,313.02 -		
	<u>INFORMATION AND BROADCASTING</u>				
	<u>National Film Archive Of India</u>				
14	NATIONAL FILM HERITAGE MISSION - [N09000001]NFAI, MAHARASHTRA	11/2014	597.41 -	- -	-
	Total		597.41 -		

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(September 2019)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>MINES</u>				
	<u>National Aluminum Company Limited (Nalco)</u>				
15	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N1000014]NALCO,TAMIL NADU	09/2017	166.62 -	06/2019 -	-
	Total		166.62 -		
	<u>PETROLEUM</u>				
	<u>Chennai Petroleum Corporation Limited</u>				
16	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU	03/2013	3,110.36 -	11/2015 -	-
	<u>Hindustan Petroleum Corporation Limited</u>				
17	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN	11/2011	310.00 -	03/2013 -	-
18	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH - [N16000311]HPCL,CHHATTISGARH	12/2016	300.00 -	04/2021 -	-
	<u>Indian Oil Corporation Limited</u>				
19	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	09/2017 -	07/2019
20	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]IOCL,BIHAR	07/2015	822.66 -	11/2018 -	08/2019
21	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	10/2015	607.06 -	10/2017 -	-
22	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]IOCL,HIMACHAL PRADESH	02/2016	151.00 -	09/2019 -	-
	<u>Indian Strategic Petroleum Reserves Ltd</u>				
23	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KARNATAKA	01/2006	993.00 -	01/2012 -	-
	<u>Mangalore Refinery And Petrochemicals Limited</u>				
24	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]MANGALORE REFIN,KARNATAKA	05/2015	224.00 207.00	04/2019 -	-
	<u>Oil India Limited</u>				
25	50MW WIND ENERGY POWER PROJECT - [N16000298]OIL,MULTI STATE	11/2015	500.00 -	06/2017 -	-
26	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	03/2015 -	-
	Total		11,039.43 -		
	<u>POWER</u>				
	<u>Chenab Valley Power Projects [P] Limited</u>				
27	KIRU HYDRO ELECTRIC PROJECT - [N18000278]CVPPPL,JAMMU AND KASHMIR	03/2019	4,287.59 -	- -	-
	<u>National Hydro-Electric Power Corporation</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(September
2019)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
28	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR	12/1999	578.62 -	06/2006 -	-
29	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-
	<u>National Thermal Power Corporation</u>				
30	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	09/2016 -	-
31	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	08/2017 -	-
32	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,238.00	10/2017 -	-
	<u>Power Grid Corporation Of India Limited</u>				
33	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 -	02/2016 -	06/2019
34	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]PGCIL,MULTI STATE	01/2015	268.80 -	03/2018 -	06/2019
35	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]PGCIL,MULTI STATE	03/2017	251.60 -	06/2019 -	06/2019
36	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 -	11/2008 -	-
	Total		27,334.24 -		
	<u>HEALTH AND FAMILY WELFARE</u>				
	<u>Hospital Services Consultancy Corporation Ltd</u>				
37	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	-
38	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	05/2017 -	-
39	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA	09/2014	505.58 -	03/2018 -	-
40	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL	08/2016	244.00 -	09/2018 -	-
	Total		1,218.80 -		
	<u>RAILWAYS</u>				
	<u>Container Corporation Of India</u>				
41	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH	01/2013	387.70 -	03/2018 -	-
42	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH	05/2014	207.00 -	03/2018 -	-
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>				
43	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	11,589.00 30,357.00	- -	-
	<u>East Central Railways</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(September
2019)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
44	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-
45	CONSTRUCTION OF ROBS IN THE STATE OF BIHAR - [N22000344]ECR,BIHAR	07/2004	599.63 674.00	12/2007 -	-
46	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 546.71	07/2014 -	-
	<u>Eastern Railways</u>				
47	PIRAPINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	05/2019
	<u>Kolkata Metro Rail Corporation Limited</u>				
48	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-
	<u>Metropolitan Rapid Transport Projects</u>				
49	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-
50	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP, TAMIL NADU	04/2006	495.74 -	06/2013 -	-
51	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	-
	<u>North Central Railway</u>				
52	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-
53	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	2,030.50 -	- -	-
	<u>North East Frontier Railway</u>				
54	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	12/2015 -	-
55	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 -	03/2019 -	-
56	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE	04/1999	819.23 -	- -	-
57	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHOWA-JAIN - [N22000499]NFR, WEST BENGAL	02/1999	380.60 -	04/2010 -	-
	<u>North Eastern Railway</u>				
58	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-
59	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
60	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
61	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-
62	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(September
2019)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
63	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH	04/2016	602.50 -	- -	-
	<u>North Western Railway</u>				
64	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-
65	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
66	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
67	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-
	<u>Rail India Technical And Economic Service</u>				
68	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-
	<u>Railway Electrification</u>				
69	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-
	<u>South Central Railway</u>				
70	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	164.36 -	02/2009 -	-
71	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	458.25 -	- -	-
72	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-
73	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-
74	GUDUR-DURGARAJPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	761.37 -	- -	-
75	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
76	KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA	04/2013	723.00 -	- -	-
77	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-
	<u>South Eastern Railway</u>				
78	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	651.00 -	03/2015 -	-
79	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-
80	CONSTRUCTION OF ROBS IN THE STATE OF BIHAR (NEW ROBS-12) - [N22000337]SER,BIHAR	08/2010	400.00 -	03/2014 -	-
81	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-
	<u>Southern Railway</u>				
82	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	1,566.00 2,815.62	- -	-
83	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	227.40 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(September 2019)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
84	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	- -	-
85	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	151.84 -	02/2019 -	-
86	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-
87	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
88	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-
89	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 457.08	- -	-
90	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 252.96	- -	-
91	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
92	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 189.24	- -	-
93	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 828.50	- -	-
94	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	03/2005 -	-
95	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-
96	ATTIPATTU - KORUKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU	02/1999	257.00 257.00	03/2018 -	-
	<u>Western Railway</u>				
97	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 03/2017	03/2017
98	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT	03/2017	243.60 -	- -	-
99	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-
100	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-
101	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-
102	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 -	- -	-
	Total		51,909.65 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
	<u>Dept Of Road Transport & Highways</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(September 2019)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
103	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA	03/2015	298.33 -	- -	-
104	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]DORTH,GOA	03/2015	184.05 -	- -	-
105	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA	03/2015	280.16 -	- -	-
<u>Ministry Of Road Transport And Highways</u>					
106	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]MORTH,ANDHRA PRADESH	01/2016	386.09 -	05/2016 08/2019	05/2018
107	AJANTHA TO BULDHANA - [N24001008]MORTH,A & N ISLANDS	02/2017	401.00 401.00	07/2019 -	07/2019
108	MANTHA TALUKAS BORDER TO PARTUR - [N24001033]MORTH,MAHARASHTRA	01/2017	486.19 486.19	07/2019 -	07/2019
109	PARTUR TO MAJALGAON - [N24001034]MORTH,MAHARASHTRA	01/2017	420.57 420.57	07/2019 -	07/2019
110	MAJALGAON TO KAIJ - [N24001036]MORTH,MAHARASHTRA	01/2017	413.99 -	07/2019 -	07/2019
111	KAIJ TO KUSALAM - [N24001037]MORTH,MAHARASHTRA	01/2017	554.78 554.78	07/2019 -	07/2019
112	SHIROD SHAHPURER TO NANDED - [N24001041]MORTH,MAHARASHTRA	01/2017	211.34 211.34	07/2019 -	07/2019
113	MUL TO CHANDRAPUR - [N24001117]MORTH,MAHARASHTRA	12/2016	162.34 -	07/2019 -	07/2019
114	KATOL TO WARUD - [N24001019]MORTH,MAHARASHTRA	01/2017	463.62 664.00	06/2019 -	08/2019
115	AMD TO SAONER - [N24001021]MORTH,MAHARASHTRA	01/2017	396.91 396.91	06/2019 -	08/2019
116	AHMADPUR TO PIMPLA - [N24001029]MORTH,MAHARASHTRA	01/2017	422.38 422.38	08/2019 -	08/2019
117	PIMPLA TO MANJARUMBHA - [N24001030]MORTH,MAHARASHTRA	01/2017	595.77 595.77	08/2019 -	08/2019
118	MANJUSUMBA TO CHUMBALI - [N24001031]MORTH,MAHARASHTRA	01/2017	228.54 228.54	08/2019 -	08/2019
119	AHMEDNAGAR TO BARAMATI - [N24001100]MORTH,MAHARASHTRA	01/2017	955.40 -	08/2019 -	08/2019
120	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA	10/2015	289.60 -	- -	-
121	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-
122	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(September
2019)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
123	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-
124	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-
125	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-
126	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-
127	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 -	08/2015 -	-
128	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-
129	CONSTRUCTION OF PAVED SHOULDERS INCLUDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I- - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-
130	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-
131	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-
132	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN	12/2015	621.43 -	06/2018 -	-
133	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-
134	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	11/2015 -	-
135	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA	01/1991	219.40 -	01/2018 -	-
136	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA	01/1991	218.63 -	10/2017 -	-
137	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-
138	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH,WEST BENGAL	01/1991	322.00 -	03/2018 -	-
139	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR	01/1991	282.41 -	08/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(September
2019)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
140	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR	01/1991	358.22 -	10/2016 -	-
141	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA	01/1991	229.41 -	05/2018 -	-
142	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-
143	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98 -	- -	-
144	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-
145	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-
146	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR	10/2013	278.39 -	08/2014 -	-
147	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR	11/2013	683.83 -	07/2016 -	-
148	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR	02/2014	665.50 -	07/2016 -	-
149	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR	02/2016	178.85 -	05/2016 -	-
150	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR	02/2016	369.77 -	06/2016 -	-
151	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR	02/2016	553.30 -	05/2016 -	-
152	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-
153	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPR - [N24000580]MORTH,BIHAR	03/2015	206.80 -	07/2016 -	-
154	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR	08/2015	288.24 -	11/2015 -	-
155	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR	08/2016	1,742.01 -	12/2016 -	-
156	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MORTH,ODISHA	01/2015	326.63 327.00	04/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(September 2019)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
157	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA	02/2015	239.91 240.00	10/2017 -	-
158	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA	07/2014	342.05 342.00	01/2017 -	-
159	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA	06/2016	157.30 157.00	06/2018 -	-
160	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MORTH,UTTARAKHAND	02/2018	293.68 -	- -	-
161	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MORTH,UTTARAKHAND	03/2018	460.73 -	- -	-
162	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26. - [N24000911]MORTH,ODISHA	03/2016	165.06 -	12/2016 -	-
163	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MORTH,ODISHA	08/2016	287.70 -	02/2017 -	-
164	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MORTH,ODISHA	09/2016	295.67 -	02/2017 -	-
165	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MORTH,ODISHA	12/2016	223.50 -	08/2018 -	-
166	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MORTH,ODISHA	12/2016	206.88 -	04/2018 -	-
167	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MORTH,ODISHA	03/2018	214.23 -	08/2018 -	-
168	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MORTH,ODISHA	03/2018	199.16 -	08/2018 -	-
169	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MORTH,BIHAR	09/2018	1,478.40 -	- -	-
170	SARSAM TO KOTHARI - [N24001002]MORTH,MAHARASHTRA	02/2016	545.64 -	07/2019 -	-
171	AKOLA TO AKOT - [N24001003]MORTH,MAHARASHTRA	01/2017	313.95 -	06/2019 -	-
172	AKOT TO ANJANGAON - [N24001006]MORTH,MAHARASHTRA	01/2017	245.77 246.00	06/2019 -	-
173	ANJANGAON TO MAH/MP BORDER - [N24001007]MORTH,MADHYA PRADESH	01/2017	359.00 359.00	06/2019 -	-
174	MEHKAR TO CHIKALI - [N24001011]MORTH,MAHARASHTRA	02/2017	322.48 322.00	05/2019 -	-
175	MORSHI TO MAH/MP BORDER - [N24001016]MORTH,MAHARASHTRA	01/2017	471.61 472.00	06/2019 -	-
176	DAHEGAON TO KUHI - [N24001017]MORTH,MAHARASHTRA	01/2017	228.89 228.89	06/2019 -	-
177	BHANDARA TO GHOTITOK - [N24001018]MORTH,MAHARASHTRA	01/2017	392.83 393.00	06/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(September
2019)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
178	JINTUR TO PARBHANI - [N24001039]MORTH,MAHARASHTRA	01/2017	356.66 356.66	- -	-
179	KALMAB TO RALEGAON - [N24001044]MORTH,MAHARASHTRA	01/2017	467.78 -	06/2019 -	-
180	RALEGAON TO RAMTIRTH - [N24001046]MORTH,MAHARASHTRA	01/2017	210.81 -	07/2019 -	-
181	MEHKAR TO AJISPUR - [N24001048]MORTH,MAHARASHTRA	01/2017	232.77 -	07/2019 -	-
182	HELWAK TO KARAD - [N24001055]MORTH,MAHARASHTRA	02/2017	416.99 -	07/2019 -	-
183	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MORTH,MAHARASHTRA	02/2017	422.02 422.00	07/2019 -	-
184	BODHWAD TO STATE BORDER - [N24001086]MORTH,MAHARASHTRA	01/2017	178.26 -	07/2019 -	-
185	KOLDE TO KHETIYA - [N24001090]MORTH,MAHARASHTRA	01/2017	509.18 -	07/2019 -	-
186	SATARA TO MHASWAD - [N24001092]MORTH,MAHARASHTRA	01/2017	653.46 -	07/2019 -	-
187	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MORTH,MAHARASHTRA	01/2017	388.44 -	- -	-
188	MHASWAD TO TEMBHURNI - [N24001099]MORTH,MAHARASHTRA	01/2017	488.60 -	07/2019 -	-
189	KURUDWADI TO PANDHARPUR - [N24001101]MORTH,MAHARASHTRA	01/2017	307.63 -	07/2019 -	-
190	PANDHARPUR TO SANGOLA - [N24001102]MORTH,MAHARASHTRA	07/2017	218.38 -	07/2019 -	-
191	SARAD VANI PIMPALGAON - [N24001103]MORTH,MAHARASHTRA	01/2017	250.46 -	07/2019 -	-
192	CHIMUR TO WARORA - [N24001105]MORTH,MAHARASHTRA	11/2016	467.70 -	03/2019 -	-
193	GADCHIROLI TO MUL - [N24001116]MORTH,MAHARASHTRA	12/2016	484.15 -	06/2019 -	-
194	NAGBHID TO ARMORI - [N24001119]MORTH,MAHARASHTRA	09/2016	269.05 -	07/2019 -	-
195	PAITHAN TO SHIRUR - [N24001122]MORTH,MAHARASHTRA	03/2017	341.80 -	06/2019 -	-
196	SHIRUR TO KHARDA - [N24001123]MORTH,MAHARASHTRA	02/2017	381.77 -	06/2019 -	-
197	AURANGABAD TO SILLOD - [N24001124]MORTH,MAHARASHTRA	02/2017	456.32 -	06/2019 -	-
198	SILLOD TO FARDAPUR - [N24001125]MORTH,MAHARASHTRA	02/2017	337.46 -	06/2019 -	-
199	FARDAPUR TO JALGAON - [N24001126]MORTH,MAHARASHTRA	02/2017	456.45 -	06/2019 -	-
200	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MORTH,MAHARASHTRA	02/2017	406.51 -	06/2019 -	-
201	BHOKAR TO SARSAM - [N24001128]MORTH,MAHARASHTRA	02/2017	295.09 -	07/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(September
2019)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
202	WAKED TO TALEGAON - [N24001135]MORTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	-
203	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MORTH,ARUNACHAL PRADESH	09/2011	1,979.00 -	- -	-
204	ALWAR-NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MORTH,RAJASTHAN	03/2019	178.13 -	- -	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>				
205	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH	07/2015	197.16 197.16	10/2018 09/2015	09/2018
206	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL,ARUNACHAL PRADESH	10/2015	210.50 210.50	- 01/2016	01/2019
207	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL,ARUNACHAL PRADESH	03/2015	194.11 -	05/2018 -	08/2019
208	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 387.00	08/2016 -	08/2019
209	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 340.00	08/2016 -	08/2019
210	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL,ASSAM	06/2016	829.00 -	01/2019 -	-
211	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM	03/2015	168.39 -	11/2018 -	-
212	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM	10/2014	588.95 -	11/2018 -	-
213	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL,ARUNACHAL PRADESH	10/2015	179.82 -	01/2019 -	-
214	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]NHIDCL,ASSAM	12/2015	225.02 -	12/2018 -	-
215	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM	12/2015	223.30 -	06/2018 -	-
216	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-
217	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM	12/2015	289.99 -	12/2018 -	-
218	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450 TO KM 605.600(EXISTING CHAINAGE FROMKM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH	01/2016	183.65 -	11/2016 -	-
219	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH	02/2017	195.23 -	04/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(September
2019)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
220	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH	02/2017	203.36 -	04/2017 -	-
221	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH	01/2017	194.66 -	04/2017 -	-
222	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND	02/2017	507.68 -	04/2017 -	-
223	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH	01/2017	198.22 -	04/2017 -	-
224	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM	04/2017	388.00 -	10/2017 -	-
225	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND	03/2018	274.31 -	05/2018 -	-
226	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND	03/2018	403.36 -	06/2018 -	-
227	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND	03/2018	417.24 -	05/2018 -	-
228	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS	03/2015	262.97 -	10/2018 -	-
229	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS	03/2017	409.85 -	12/2017 -	-
230	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS	03/2015	277.17 -	04/2017 -	-
231	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS	02/2018	391.00 -	10/2018 -	-
232	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS	03/2018	234.27 -	10/2018 -	-
233	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND	02/2017	387.00 -	09/2018 -	-
234	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND	03/2018	500.09 -	09/2018 -	-
235	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND	03/2018	339.57 233.35	09/2018 07/2019	-
236	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND	03/2018	239.30 -	09/2018 05/2019	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(September 2019)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
237	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND	03/2018	285.68 -	09/2018 -	-
238	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND	03/2018	315.03 -	09/2018 -	-
239	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND	03/2018	240.64 -	09/2018 -	-
240	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND	03/2018	237.72 136.73	09/2018 11/2018	-
241	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND	03/2018	251.97 160.10	09/2018 11/2018	-
242	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND	03/2018	282.98 -	09/2018 11/2018	-
243	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND	03/2018	215.12 -	09/2018 -	-
244	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND	03/2018	215.79 -	09/2018 -	-
245	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND	03/2018	272.89 -	09/2018 -	-
246	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND	03/2018	323.98 -	09/2018 -	-
247	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA - [N24000766]NHIDCL,SIKKIM	04/2017	318.42 -	11/2017 -	-
248	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM	03/2017	375.80 -	- -	-
249	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM	11/2017	290.05 -	11/2017 -	-
250	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM	03/2018	264.84 -	06/2018 -	-
251	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITA AND PANITNAKI I - [N24000770]NHIDCL,WEST BENGAL	03/2017	158.65 -	06/2018 -	-
252	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM	03/2015	829.00 -	01/2016 -	-
253	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL,UTTARAKHAND	03/2018	1,383.78 -	07/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(September 2019)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
254	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866])NHIDCL,JAMMU AND KASHMIR	03/2018	404.17 -	08/2018 -	-
255	WIDENING AND UPGADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM - [N24000867]NHIDCL,JAMMU AND KASHMIR	03/2018	216.00 -	11/2018 -	-
256	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR	03/2018	253.44 -	07/2019 -	-
257	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA	03/2019	306.28 -	05/2019 -	-
258	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH	12/2016	200.44 -	- -	-
259	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH	03/2017	1,718.59 -	- -	-
260	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 37.500 TO KM - [N24000947]NHIDCL,ARUNACHAL PRADESH	05/2016	259.52 -	- -	-
261	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH	09/2016	568.92 -	- -	-
262	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH	12/2016	188.78 -	- -	-
263	BORDUMSA NAMCHIK (BURIDEHING - JAIRAMPUR) ROAD ON NH-52B (NEW NH-215) FROM KM. 0.15 (STARTING CHAIN - [N24000977]NHIDCL,ARUNACHAL PRADESH	07/2015	189.91 -	- -	-
264	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN - [N24000978]NHIDCL,ARUNACHAL PRADESH	03/2015	172.75 -	- -	-
265	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI - [N24000979]NHIDCL,ARUNACHAL PRADESH	01/2017	256.66 -	- -	-
266	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL,ASSAM	03/2017	1,049.51 -	- -	-
National Highways Authority Of India					
267	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 -	03/2019 -	07/2019
268	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 255.23	11/2008 01/2011	08/2013
269	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 408.77	11/2008 07/2011	01/2014
270	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- 06/2015	06/2015
271	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- 06/2015	06/2015

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(September 2019)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
272	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 03/2018	03/2018
273	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	04/2018 08/2018	08/2018
274	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 655.17	07/2009 10/2018	10/2018
275	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA	09/2016	1,004.67 -	05/2019 -	02/2019
276	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 -	03/2019
277	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 315.00	- 03/2020	03/2019
278	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 -	06/2019
279	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	02/2019 -	06/2019
280	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 456.92	02/2009 07/2019	07/2019
281	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	04/2010 -	07/2019
282	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	11/2017 -	07/2019
283	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 340.14	04/2009 03/2011	08/2019
284	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH	08/2016	227.49 -	01/2019 -	08/2019
285	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 3,787.21	09/2012 12/2019	-
286	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 2,848.49	08/2011 -	-
287	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	-
288	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-
289	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-
290	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 2,519.00	06/2015 -	-
291	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-
292	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	-
293	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	-
294	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(September
2019)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
295	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	-
296	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	-
297	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	-
298	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-
299	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	-
300	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-
301	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	-
302	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	-
303	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	-
304	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	-
305	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	-
306	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	-
307	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	06/2015 -	-
308	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-
309	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 2,521.24	12/2015 -	-
310	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	04/2015 -	-
311	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	02/2014 -	-
312	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	-
313	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA	08/2015	723.54 -	02/2018 -	-
314	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	-
315	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	01/2016 -	-
316	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	-
317	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH	06/2014	301.04 -	01/2016 -	-
318	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	01/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(September
2019)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
319	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI, MAHARASHTRA	07/2015	2,288.18 -	05/2019 -	-
320	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI, MAHARASHTRA	07/2015	1,885.74 -	05/2019 -	-
321	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI, RAJASTHAN	08/2014	822.90 -	04/2018 -	-
322	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI, MULTI STATE	09/2015	788.51 -	03/2018 -	-
323	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI, HARYANA	07/2015	2,128.72 -	04/2019 -	-
324	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI, UTTAR PRADESH	09/2015	785.78 -	03/2018 -	-
325	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI, UTTAR PRADESH	07/2015	1,657.20 -	01/2019 -	-
326	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI, UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-
327	NAGPUR - KONDHALI - [N24000472]NHAI, MAHARASHTRA	09/2005	168.00 -	06/2006 -	-
328	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI, BIHAR	08/2015	556.07 -	- -	-
329	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI, RAJASTHAN	02/2008	1,673.70 -	10/2011 -	-
330	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI, BIHAR	12/2015	1,041.10 -	04/2019 -	-
331	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI, HARYANA	11/2015	867.66 -	05/2018 -	-
332	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI, MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	-
333	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI, MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	-
334	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI, MADHYA PRADESH	06/2015	1,583.79 -	01/2019 -	-
335	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI, MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	-
336	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL	04/2014	1,665.00 -	- -	-
337	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI, BIHAR	08/2015	854.80 -	- -	-
338	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI, BIHAR	08/2015	516.13 -	04/2018 -	-
339	TRICHY - KARUR - [N24000528]NHAI, TAMIL NADU	03/2007	516.00 -	07/2008 -	-
340	MEERUT-BULANDSHAHAH - [N24000539]NHAI, UTTAR PRADESH	01/2016	683.24 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(September
2019)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
341	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 -	07/2018 -	-
342	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	04/2019 -	-
343	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHILIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	11/2018 -	-
344	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-
345	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 TO 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-
346	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	- -	-
347	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	- -	-
348	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 241.41	- -	-
349	BALANCE WORK OF 4 LANING OF GORAKHPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	-
350	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	10/2018 -	-
351	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]NHAI,DELHI	09/2015	771.18 -	- -	-
352	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-
353	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-
354	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH	09/2017	374.40 -	09/2017 -	-
355	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27 -	- -	-
356	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	- -	-
357	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-
358	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- -	-
359	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(September 2019)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
360	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI, BIHAR	01/2018	573.70 -	- -	-
361	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI, BIHAR	01/2018	895.39 -	- -	-
362	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI, JHARKHAND	01/2018	273.46 -	- -	-
363	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI, JHARKHAND	01/2018	1,155.16 -	- -	-
364	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI, MADHYA PRADESH	01/2018	770.73 -	- -	-
365	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI, ODISHA	01/2018	633.68 -	- -	-
366	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM - [N24000737]NHAI, ODISHA	01/2018	1,522.00 -	- -	-
367	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI, ODISHA	01/2018	999.00 -	- -	-
368	VARANASI RING ROAD PKG - I - [N24000740]NHAI, UTTAR PRADESH	01/2018	450.77 929.89	- -	-
369	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI, TELANGANA	03/2017	4,429.00 -	03/2017 -	-
370	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI, KARNATAKA	02/2018	486.78 -	- -	-
371	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI, KERALA	02/2018	1,424.77 -	- -	-
372	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI, UTTAR PRADESH	02/2018	670.50 -	- -	-
373	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI, WEST BENGAL	03/2018	1,261.98 -	- -	-
374	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI, UTTAR PRADESH	03/2018	809.07 -	- -	-
375	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI, UTTAR PRADESH	03/2018	925.40 -	- -	-
376	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI, RAJASTHAN	02/2018	741.86 -	- -	-
377	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI, RAJASTHAN	02/2018	716.76 -	- -	-
378	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI, UTTAR PRADESH	03/2018	2,140.93 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(September
2019)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
379	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI, UTTAR PRADESH	03/2018	1,120.57 -	- -	-
380	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI, UTTAR PRADESH	03/2018	1,025.80 -	- -	-
381	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI, UTTAR PRADESH	03/2018	1,115.28 -	- -	-
382	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K - [N24000804]NHAI, TELANGANA	03/2018	802.65 -	- -	-
383	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI, ARUNACHAL PRADESH	03/2018	392.60 -	- -	-
384	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI, BIHAR	03/2018	496.20 -	- -	-
385	FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI, TELANGANA	03/2018	950.63 -	- -	-
386	FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI, TELANGANA	03/2018	857.62 -	- -	-
387	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI, TELANGANA	03/2018	828.29 -	- -	-
388	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI, TAMIL NADU	03/2018	633.55 -	- -	-
389	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI, TAMIL NADU	03/2018	2,065.96 -	- -	-
390	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI, MULTI STATE	03/2018	1,294.47 -	- -	-
391	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI, MULTI STATE	03/2018	998.70 -	- -	-
392	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI, RAJASTHAN	03/2018	874.25 -	- -	-
393	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI, RAJASTHAN	03/2018	1,158.35 -	- -	-
394	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI, PUNJAB	03/2018	199.90 149.90	- -	-
395	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - [N24001185]NHAI, UTTAR PRADESH	11/2017	2,159.00 -	01/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(September 2019)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
396	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI,HARYANA	01/2019	1,051.91 -	- -	-
397	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI,HARYANA	01/2019	1,120.06 -	- -	-
398	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA	01/2019	1,137.42 -	- -	-
399	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA	01/2019	1,033.19 -	- -	-
400	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA	01/2019	1,243.45 -	- -	-
401	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA	01/2019	889.36 -	- -	-
402	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA	01/2019	1,018.79 -	- -	-
403	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA	01/2019	996.65 -	- -	-
404	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI,MADHYA PRADESH	10/2019	743.88 -	- -	-
405	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 275.00	05/2017 -	-
406	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	12/2017 -	-
	<u>National Highways Development Project</u>				
407	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]NHDP,GOA	03/2015	297.00 -	04/2018 -	-
408	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA	03/2015	168.30 -	- -	-
409	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA	01/2014	446.77 -	- -	-
410	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	- -	-
	<u>Public Works Dept Of State</u>				
411	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O - [N24000871]PWD,WEST BENGAL	08/2014	600.87 720.97	11/2017 05/2019	05/2019
412	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873]PWD,WEST BENGAL	08/2014	823.20 937.76	11/2017 06/2019	06/2019
413	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]PWD,WEST BENGAL	04/2014	279.70 398.52	08/2017 07/2019	07/2019
414	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2 - - [N24001147]PWD,UTTAR PRADESH	10/2016	239.63 -	02/2019 -	07/2019
415	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 - [N24000962]PWD,MADHYA PRADESH	09/2016	178.23 -	09/2018 -	08/2019

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(September 2019)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
416	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]PWD,TELANGANA	01/2017	359.27 -	05/2019 -	08/2019
417	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNASAGAR DAM SECT - [N24000245]PWD,TELANGANA	01/2014	270.00 -	03/2016 -	-
418	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOIA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA	08/2014	187.79 -	07/2016 -	-
419	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH	07/2015	333.21 333.21	12/2015 -	-
420	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH	12/2015	291.05 -	- -	-
421	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH	01/2014	195.45 -	11/2014 -	-
422	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH	11/2015	485.44 -	12/2015 -	-
423	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	-
424	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-
425	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-
426	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 389.45	05/2012 06/2018	-
427	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 203.26	08/2013 -	-
428	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-
429	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE - [N24000373]PWD,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	-
430	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	-
431	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM	11/2010	268.08 -	05/2017 -	-
432	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	-
433	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(September
2019)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
434	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM	11/2014	218.31 307.47	02/2018 -	-
435	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA	07/2014	342.05 -	01/2017 -	-
436	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	-
437	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	-
438	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	-
439	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-
440	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-
441	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA	03/2016	1,142.62 -	- -	-
442	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA	03/2016	1,101.58 -	- -	-
443	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]PWD,WEST BENGAL	01/2017	396.86 396.86	09/2019 -	-
444	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]PWD,UTTAR PRADESH	11/2016	326.99 327.00	- -	-
445	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) - [N24000908]PWD,HARYANA	01/2017	276.01 -	03/2019 07/2019	-
446	WIDENING FROM TWO LANE TO FOUR LANE WITH PAVED SHOULDER AND STRENGTHNING OF EXISTING PAVEMENT BETWEE - [N24000920]PWD,GUJARAT	03/2016	223.67 -	02/2017 -	-
447	UPGRADATION TO 2 LANE WITH PAVED SHOULDER WITH RIGID PAVEMETS FROM 37/400 TO KM 66/700 ON NH 848 ON - [N24000921]PWD,GUJARAT	03/2016	208.34 -	02/2016 -	-
448	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922]PWD,GUJARAT	12/2017	867.97 -	11/2018 -	-
449	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEE - [N24000923]PWD,GUJARAT	03/2018	464.07 -	11/2018 -	-
450	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]PWD,GUJARAT	10/2018	400.76 -	05/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(September 2019)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
451	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926]PWD, GUJARAT	08/2017	962.43 -	03/2018 -	-
452	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552-EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950]PWD, RAJASTHAN	11/2017	187.82 -	04/2018 -	-
453	NETRA VILLAGE TO MANDORE SECTION OF NH-65 KM 267+500 TO 296+070 (4L) UNDER EPC. - [N24000951]PWD, RAJASTHAN	10/2014	382.81 -	01/2015 -	-
454	UP-GRADATION TO TWO LANE WITH PAVED SHOULDER FOR SECTION FROM KM 58.000 TO KM 91.600 (BALOTRA TO SAN - [N24000952]PWD, RAJASTHAN	01/2017	179.32 -	11/2017 -	-
455	CONSTRUCTION OF NAGPUR BYPASS FROM EXISTING KM 166/260 TO KM 180/500 OF NH-65 ON EPC MODE. - [N24000953]PWD, RAJASTHAN	03/2016	155.77 -	09/2016 -	-
456	NAGPUR-BIKANER OF NH-11 (2L+PS) UNDER PPP. - [N24000954]PWD, RAJASTHAN	01/2012	378.07 478.73	01/2014 -	-
457	CITTORGARH-NEEMACH (4L) OF NH-79 AND NIMBAHARA PRATAPGARH (2L+PS) OF NH-113 UNDER PPP. - [N24000955]PWD, RAJASTHAN	10/2012	511.21 -	10/2013 -	-
458	DEVELOPMENT AND OPERATION OF BIKANER- SURATGARH SECTION OF NH-15 BY 2L+PS IN THE STATE OF RAJASTHAN - [N24000956]PWD, RAJASTHAN	03/2009	501.00 671.54	09/2013 -	-
459	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709 - [N24000957]PWD, RAJASTHAN	11/2017	163.95 -	04/2018 -	-
460	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000958]PWD, RAJASTHAN	02/2018	370.30 -	06/2018 -	-
461	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000959]PWD, RAJASTHAN	02/2018	341.79 -	05/2018 -	-
462	CONSTRUCTION OF 4 LANING BY CC PAVEMENT ON KOTA-DARAH OF NH-12 FROM 256/550 TO 289/550 UNDER EPC. - [N24000960]PWD, RAJASTHAN	12/2015	621.43 -	10/2016 -	-
463	UP-GRADATION TO 2 LANE WITH PAVED SHOULDER FOR SECTION FROM KM 118.900 TO KM 156.955 BALOTRA TOSANDE - [N24000961]PWD, RAJASTHAN	01/2017	163.54 -	07/2017 -	-
464	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037 OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]PWD, TELANGANA	01/2017	244.54 -	05/2019 09/2019	-
465	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]PWD, TELANGANA	01/2019	193.19 -	- -	-
466	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]PWD, BIHAR	03/2018	153.24 -	- -	-
467	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT - [N24001154]PWD, KARNATAKA	08/2016	367.44 -	01/2017 -	-
468	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT - [N24001155]PWD, KARNATAKA	08/2016	175.20 -	01/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(September 2019)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
469	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA - [N24001156]PWD,KARNATAKA	01/2017	166.67 -	09/2017 -	-
470	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]PWD,KARNATAKA	08/2016	175.50 -	02/2017 -	-
471	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]PWD,KARNATAKA	03/2018	159.97 -	06/2019 -	-
472	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHAARA SECTION - [N24001159]PWD,KARNATAKA	01/2018	159.70 -	07/2018 -	-
473	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]PWD,KARNATAKA	09/2017	191.60 -	10/2018 -	-
474	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]PWD,KARNATAKA	12/2017	297.30 -	01/2019 -	-
475	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]PWD,KARNATAKA	03/2018	325.86 -	10/2018 -	-
476	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]PWD,KARNATAKA	08/2016	329.01 -	02/2017 -	-
477	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]PWD,KARNATAKA	10/2016	396.96 -	03/2017 -	-
478	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]PWD,KARNATAKA	11/2016	314.90 -	03/2017 -	-
479	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]PWD,KARNATAKA	03/2015	159.12 -	01/2016 -	-
480	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776) - [N24001167]PWD,KARNATAKA	03/2015	165.67 -	01/2016 -	-
481	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM. - [N24001170]PWD,KARNATAKA	01/2014	471.16 -	08/2014 -	-
482	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]PWD,KARNATAKA	01/2017	291.49 -	08/2017 -	-
483	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S - [N24001183]PWD,ANDHRA PRADESH	07/2014	251.55 -	02/2015 -	-
484	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]PWD,ARUNACHAL PRADESH	11/2016	243.89 -	- -	-
485	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]PWD,BIHAR	02/2019	2,926.42 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(September 2019)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
486	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]PWD,UTTAR PRADESH	03/2018	306.59 -	- -	-
487	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]PWD,UTTAR PRADESH	11/2018	281.45 -	- -	-
	Total		2,28,192.82 -		
	<u>TELECOMMUNICATIONS</u>				
	<u>Indian Telephone Industry</u>				
488	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI,MULTI STATE	09/2014	2,111.17 -	09/2014 -	-
	<u>Mahanagar Telephone Nigam Limited</u>				
489	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI	06/2016	418.26 -	06/2017 -	-
	Total		2,529.43 -		
	<u>URBAN DEVELOPMENT</u>				
	<u>Central Public Works Department</u>				
490	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	03/2012 -	-
491	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH	06/2014	157.84 -	03/2017 -	-
492	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	12/2015 -	-
493	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL	10/2014	162.88 -	04/2018 -	-
494	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]CPWD,DELHI	12/2017	188.00 -	06/2019 -	-
495	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP - [N28000108]CPWD,ANDHRA PRADESH	01/2018	206.58 -	03/2019 -	-
496	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI	10/2016	248.20 -	04/2018 -	-
497	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI - [N28000123]CPWD,DELHI	07/2017	218.72 -	- -	-
	<u>Chennai Metro Rail Ltd</u>				
498	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 -	12/2015 -	-
499	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU	06/2016	3,770.00 -	03/2018 -	-
	<u>Hindustan Steelwork Construction Limited</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(September
2019)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
500	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	12/2015 -	-
501	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	12/2016 -	-
502	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	12/2016 -	-
503	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,070.97	02/2014 -	-
504	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 324.87	12/2015 -	-
505	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	09/2017 -	-
506	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	- -	-
507	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL,GUJARAT	01/2013	175.00 -	- -	-
508	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	03/2017 -	-
509	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 253.92	06/2016 -	-
510	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND	12/2007	200.00 -	03/2018 -	-
511	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	12/2016 -	-
512	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND	04/2013	170.00 -	04/2018 -	-
513	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL	08/2012	185.37 -	03/2016 -	-
	<u>Jawahar Lal Nehru National Urban Renewal Mission</u>				
514	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-
	<u>Lucknow Metro Rail Corporation Limited</u>				
515	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	-
	<u>Maharashtra Metro Rail Corporation Ltd.</u>				
516	DELHI MRTS PHASE-III - [N28000056]MMRC,DELHI	09/2011	38,585.00 -	03/2016 -	-
	<u>National Building Construcion Corporation Ltd</u>				
517	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI	07/2016	2,694.00 -	- -	-
	Total		73,060.91 -		

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(September 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	Grand Total		4,05,362.33		

Details of Projects Without Original Date of Commissioning

Annexure - IX

Costing Rs. 150 Crore and above (September 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>COAL</u>								
	<u>Singareni Colliers Company Limited</u>								
1	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL,TELANGANA	11/2016	272.73 -	272.73	162.62	- 04/2017	03/2020	35(R3)	0/6
2	RAMPURAM SHAFT BLOCK - [N06000174]SCCL,TELANGANA	08/2016	431.92 -	431.92	-	- 03/2023	-	-	0/9
3	SRAVANAPALLI OPENCAST PROJECT - [N06000175]SCCL,TELANGANA	02/2018	412.70 -	412.70	.11	- 03/2023	-	-	0/7
	Total		1,117.35 -	1,117.35	162.73				0/22
	<u>PETROLEUM</u>								
	<u>Indian Oil Corporation Limited</u>								
4	LPG BP PROJECT JODHPUR - [N16000318]IOCL,RAJASTHAN	03/2018	229.80 -	229.80	69.24	- -	03/2021	-	9/26
5	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT - [N16000336]IOCL,GUJARAT	03/2018	588.20 -	588.20	.94	- -	08/2022	-	8/17
	Total		818.00 -	818.00	70.18				17/43
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Hospital Services Consultancy Corporation</u>								
6	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH	03/2018	601.02 -	601.02	85.04	- -	02/2020	-	0/0
7	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA	03/2018	582.99 -	582.99	112.97	- -	02/2020	-	0/0
8	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC,WEST BENGAL	04/2018	651.99 -	651.99	112.82	- -	02/2020	-	0/0
9	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH	03/2018	268.84 -	268.84	99.26	- -	04/2020	-	0/0
10	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA	01/2018	249.01 -	249.01	73.40	- -	05/2020	-	0/0
	<u>Hospital Services Consultancy Corporation Ltd</u>								
11	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI	12/2017	156.56 -	156.65	54.94	- -	02/2020	-	0/0
	Total		2,510.41 -	2,510.50	538.43				0/0
	<u>RAILWAYS</u>								

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (September 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	East Central Railways								
12	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR,BIHAR	04/1998	180.82 726.31	726.31	502.13	- -	10/2019	-	0/0
13	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 367.17	425.17	406.05	- -	01/2020	-	0/0
14	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	1,033.07 3,020.95	3,376.00	3,307.82	- -	03/2021	-	0/0
15	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 1,625.87	1,625.87	508.33	- -	03/2021	-	0/0
16	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR	04/1999	325.00 735.20	735.20	362.10	- -	03/2021	-	0/0
17	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 1,470.50	1,470.50	777.71	- -	03/2021	-	0/0
18	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]ECR,BIHAR	04/1991	329.39 803.11	1,483.14	1,029.84	- -	12/2021	-	0/0
19	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 614.45	614.45	305.83	- -	03/2022	-	0/0
20	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR	04/2006	378.56 -	2,609.00	376.63	- -	03/2022	-	0/0
21	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 519.33	519.33	143.36	- -	02/2023	-	0/0
22	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 2,066.78	2,066.78	1,436.88	- -	03/2023	-	0/0
23	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	1,605.17 1,605.17	1,605.17	23.49	- 03/2023	03/2023	0(R3)	0/0
24	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	620.57	.28	- -	03/2024	-	0/0
25	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR	04/2008	326.20 -	2,995.01	1.94	- -	03/2024	-	0/0
26	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	228.05	1.53	- -	03/2024	-	0/0
27	ARA-BHABHUA ROAD (NL) - [N22000166]ECR,BIHAR	04/2008	633.87 -	633.87	.40	- -	03/2023	-	0/0
28	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR	04/2008	445.25 -	445.25	1.14	- -	03/2024	-	0/0
29	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE	04/2008	415.67 -	549.75	15.54	- -	03/2024	-	0/0
30	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	205.00	5.21	- -	03/2024	-	0/0
31	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	1,006.00	24.16	- -	03/2024	-	0/0
32	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	678.62	17.20	- -	03/2024	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (September 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
33	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	192.56	.39	-	03/2024	-	0/0
34	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	281.30	.60	-	03/2024	-	0/0
	<u>Eastern Railways</u>								
35	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	382.90	382.90	-	03/2020	-	0/0
36	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	245.41	245.41	-	03/2021	-	0/0
37	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64 -	272.20	166.12	-	09/2021	-	0/0
38	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	310.70	263.08	-	03/2024	-	0/0
39	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	1,261.34	-	-	03/2025	-	0/0
40	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	260.10	10.73	-	03/2025	-	0/0
41	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	174.56	71.42	-	03/2025	-	0/0
42	BARIARPIUR-MANANPUR VIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	250.55	20.12	-	03/2025	-	0/0
43	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	527.54	1.76	-	03/2025	-	0/0
44	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKAPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	298.22	52.09	-	03/2025	-	0/0
45	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	336.96	70.20	-	03/2025	-	0/0
46	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF ARRIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	166.89	.02	-	03/2025	-	0/0
	<u>Metropolitan Rapid Transport Projects</u>								
47	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	268.52	.03	-	03/2025	-	0/0
	<u>North East Frontier Railway</u>								
48	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 -	394.28	272.88	-	03/2021	-	0/0
49	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	333.76 -	360.00	6.67	-	03/2022	0(R3)	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above

(September 2019)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
50	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 -	380.00	38.18	- 03/2022	03/2022	0(R3)	0/0
	<u>Northern Railway</u>								
51	HARIDWAR-LAKSAR - [N22000289]NR, UTTARAKHAND	04/2012	219.83 -	346.63	229.48	- -	06/2020	-	0/0
52	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR, MULTI STATE	04/2007	336.91 -	800.00	512.67	- -	03/2022	-	0/0
53	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR, DELHI	04/2012	295.68 -	295.68	79.53	- -	03/2023	-	0/0
54	UNCHAHAR-AMETHI - [N22000294]NR, UTTAR PRADESH	04/2012	1,229.00 -	1,230.00	103.17	- -	03/2023	-	0/0
55	GRADE SEPARATOR AT DAYABASTI - [N22000269]NR, DELHI	04/1999	156.65 -	197.17	107.86	- -	03/2024	-	0/0
56	QADIAN-BEAS - [N22000295]NR, PUNJAB	04/2011	205.22 -	205.22	1.89	- -	03/2024	-	0/0
	<u>Rail Vikas Nigam Ltd.</u>								
57	RAYADURGA-TUMKUR NL - [N22000279]RVNL, MULTI STATE	04/2007	2,062.30 -	2,062.20	825.58	- -	03/2022	-	0/2
	<u>South East Central Railway</u>								
58	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, MADHYA PRADESH	04/2005	383.79 -	1,413.76	1,324.64	- -	10/2019	-	0/0
	<u>South Eastern Railway</u>								
59	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	620.00	40.99	- 03/2025	03/2025	0(R3)	0/0
	<u>South Western Railway</u>								
60	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR, KARNATAKA	04/2011	1,801.01 -	1,801.01	44.36	- -	12/2023	-	0/0
61	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR, KARNATAKA	04/2013	558.00 -	692.43	-	- -	12/2023	-	0/0
62	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR, MULTI STATE	04/2013	296.00 -	466.65	-	- -	12/2023	-	0/0
63	WHITE FIELD-KOLAR NL - [N22000280]SWR, KARNATAKA	04/2011	348.85 -	348.85	.35	- -	12/2023	-	0/0
64	TORANAGALLU-RANJITPURA DL - [N22000298]SWR, KARNATAKA	04/2011	146.75 -	167.50	.34	- -	12/2023	-	0/0
65	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR, KARNATAKA	04/2013	327.25 -	367.77	-	- -	12/2023	-	0/0
66	HUBLI-ANKOLA(NL), SWR - [220100193]SWR, KARNATAKA	04/1997	2,315.00 -	2,135.00	144.76	- -	12/2024	-	0/0
	<u>Southern Railway</u>								
67	MADURAI-BODINAYAKKANUR - [N22000201]SR, TAMIL NADU	04/2008	164.41 -	450.00	151.50	- -	03/2020	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above						(September 2019)			
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
68	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	931.98 -	951.24	724.96	- -	03/2020	-	0/0
69	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 1,431.90	1,431.90	75.00	- 06/2022	-	-	0/0
	<u>Western Railway</u>								
70	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	844.10 844.10	844.10	97.74	- 03/2021	03/2021	0(R3)	0/0
	Total		29,284.51 -	47,810.18	15,314.99				0/2
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
71	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL,ASSAM	10/2017	818.00 -	818.00	60.08	- -	06/2020	-	0/4
72	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH	04/2016	245.79 -	245.79	98.37	- -	09/2020	-	2/4
73	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH	11/2015	434.06 -	434.06	131.32	- -	12/2020	-	2/4
74	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D - [N24000974]NHIDCL,ARUNACHAL PRADESH	02/2017	199.02 199.02	199.02	9.81	- 02/2018	02/2021	36(R3)	0/0
75	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D - [N24000975]NHIDCL,ARUNACHAL PRADESH	02/2017	184.88 184.88	184.88	6.19	- 02/2018	02/2021	36(R3)	0/0
76	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA	04/2017	553.51 -	553.51	27.90	- -	09/2021	-	0/4
77	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH	02/2017	175.06 175.06	175.06	12.06	- 04/2019	04/2022	36(R3)	0/0
78	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL,ARUNACHAL PRADESH	02/2017	176.12 176.12	176.12	11.82	- 04/2019	04/2022	36(R3)	0/0
	<u>National Highways Authority Of India</u>								

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (September 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
79	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	723.64	321.67	- -	09/2019	-	0/0
80	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT	12/2016	417.19 -	417.19	262.83	- -	09/2019	-	0/0
81	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	531.00	433.62	- -	09/2019	-	0/0
82	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	941.00	824.26	- -	10/2019	-	0/0
83	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 622.00	622.00	629.18	- -	10/2019	-	0/0
84	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 622.00	622.00	582.73	- -	10/2019	-	0/0
85	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	275.90	257.52	- 02/2016	10/2019	44(R3)	0/0
86	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT	05/2016	834.64 -	834.64	140.44	- -	10/2019	-	0/0
87	FOUR LANING WITH PS TALEBANI - SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	752.28	-	- -	11/2019	-	0/0
88	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 881.00	688.70	701.76	- 05/2017	11/2019	30(R3)	0/0
89	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	447.75	179.17	- -	11/2019	-	0/0
90	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	328.67	176.29	- -	11/2019	-	0/0
91	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	1,167.45	113.26	- -	12/2019	-	0/0
92	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	392.00	240.57	- -	12/2019	-	0/0
93	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	458.03	303.12	- 12/2017	12/2019	24(R3)	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (September 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
94	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	1,100.19	900.00	- -	12/2019	-	0/0
95	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI,WEST BENGAL	10/2015	361.15 -	361.15	144.71	- -	01/2020	-	0/0
96	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	814.04	384.48	- -	01/2020	-	0/0
97	4-LANNING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	1,668.00	946.08	- -	01/2020	-	0/0
98	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	829.97	75.08	- -	01/2020	-	0/0
99	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB	03/2018	196.05 149.90	196.05	143.03	- -	01/2020	-	0/0
100	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	1,443.00	1,246.85	- -	02/2020	-	0/0
101	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	1,244.10	1,335.00	- -	02/2020	-	0/0
102	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	479.00	453.59	- -	03/2020	-	0/0
103	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	1,069.65	502.75	- -	03/2020	-	0/0
104	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	379.90	100.76	- -	03/2020	-	0/0
105	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 3,207.63	1,087.00	473.11	- 02/2018	03/2020	25(R3)	0/0
106	CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	557.30	177.12	- -	03/2020	-	0/0
107	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA	03/2018	275.12 -	275.12	119.66	- -	03/2020	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (September 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
108	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTING - [N24000837]NHAI,HARYANA	03/2018	307.79 -	307.79	140.10	- -	03/2020	-	0/0
109	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA	03/2018	198.05 -	198.05	87.04	- -	03/2020	-	0/0
110	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA	03/2018	551.58 -	551.58	243.38	- -	03/2020	-	0/0
111	4 LANNING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	1,282.94	210.80	- -	04/2020	-	0/0
112	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	1,737.00	1,159.07	- -	04/2020	-	0/0
113	4 LANNING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 1,367.00	1,169.61	1,063.10	- -	04/2020	-	0/0
114	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN	09/2016	1,239.82 -	1,239.82	1,280.27	- -	05/2020	-	3/4
115	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA	03/2018	181.78 -	181.78	52.50	- -	06/2020	-	0/0
116	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	1,408.00	442.70	- -	07/2020	-	0/0
117	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	1,273.71	-	- -	07/2020	-	0/0
118	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE-- [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	1,031.95	367.00	- -	08/2020	-	0/0
119	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 2,170.44	1,583.18	234.67	- -	09/2020	-	0/0
120	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN	02/2018	1,103.88 -	1,103.88	267.65	- -	09/2020	-	0/0
121	FOUR LANNING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	642.41	131.71	- -	10/2020	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (September 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
122	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	720.00	285.96	- 10/2020	10/2020	0(R3)	0/0
123	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 448.18	448.18	102.43	- -	10/2020	-	0/0
124	FOUR LANING OF CHETTICKULAM TO NATHAM SECTION OF NH-785 FROM CHETTICKULAM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35 -	505.35	36.14	- -	11/2020	-	0/0
125	FOUR LANING OF MADURAI- CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICKULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	628.71	59.22	- -	11/2020	-	0/0
126	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53 -	291.53	30.82	- 11/2020	11/2020	0(R3)	0/0
127	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21 -	289.21	27.22	- -	11/2020	-	0/0
128	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJI WAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	1,308.73	99.68	- -	12/2020	-	0/0
129	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43 -	314.43	24.90	- -	12/2020	-	0/0
130	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA	03/2018	1,484.30 -	1,484.30	45.34	- -	12/2020	-	0/0
131	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA	03/2018	642.13 -	807.00	302.29	- -	12/2020	-	0/0
132	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG V)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	1,251.11	1,084.26	- -	01/2021	-	0/0
133	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR	12/2017	1,471.75 1,339.00	1,339.00	376.15	- -	01/2021	-	1/3
134	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB	02/2018	261.76 -	207.00	62.85	- -	01/2021	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above						(September 2019)			
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
135	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI, GUJARAT	02/2018	1,052.21 1,449.00	1,449.00	1,296.87	- -	01/2021	-	0/0
136	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI, GUJARAT	03/2018	2,702.05 -	2,702.05	-	- -	01/2021	-	0/0
137	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI, TAMIL NADU	02/2018	1,166.26 -	1,166.26	-	- -	02/2021	-	0/0
138	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI, ANDHRA PRADESH	03/2018	565.09 -	565.09	120.20	- -	02/2021	-	0/0
139	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI, ODISHA	10/2016	1,008.96 -	1,008.96	469.78	- -	03/2021	-	0/0
140	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI, CHHATISGARH	03/2018	1,029.96 -	1,261.05	97.55	- 03/2021	03/2021	0(R3)	0/0
141	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI, JHARKHAND	03/2018	1,005.08 1,073.10	1,005.08	-	- 03/2019	03/2021	24(R3)	0/0
142	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI, MAHARASHTRA	01/2018	621.00 565.02	621.00	303.91	- 10/2018	04/2021	30(R3)	2/3
143	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI, TAMIL NADU	03/2018	1,016.92 -	1,071.00	-	- -	04/2021	-	0/0
144	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI, ODISHA	03/2018	806.11 -	806.11	6.78	- -	04/2021	-	0/0
145	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI, HIMACHAL PRADESH	03/2018	478.74 1,071.75	478.74	15.06	- -	05/2021	-	0/0
146	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI, ODISHA	12/2017	686.65 -	686.65	80.87	- 07/2020	06/2021	11(R3)	0/0
147	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI, ODISHA	12/2017	417.51 -	417.51	8.42	- -	06/2021	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above						(September 2019)			
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
148	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	953.09	109.21	- 05/2020	06/2021	13(R3)	0/0
149	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	668.86	109.20	- 05/2020	06/2021	13(R3)	0/0
150	REHABILITATION AND UPGADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	686.65	75.79	- 03/2020	06/2021	15(R3)	0/0
151	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	503.88	-	- -	06/2021	-	0/0
152	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA	11/2016	1,071.61 -	1,071.61	365.61	- -	07/2021	-	1/4
153	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA	11/2016	1,064.88 -	1,064.88	-	- -	07/2021	-	0/4
154	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	1,323.15	345.33	- -	07/2021	-	0/0
155	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 -	1,959.00	597.16	- -	07/2021	-	0/0
156	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 -	1,550.98	569.27	- -	07/2021	-	0/0
157	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64 1,687.00	1,437.64	457.31	- 12/2018	07/2021	31(R3)	0/0
158	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA	03/2018	634.70 931.21	931.21	2.55	- -	07/2021	-	0/0
159	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA	03/2018	795.50 -	799.30	80.90	- -	07/2021	-	0/0
160	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 -	1,162.92	14.29	- -	07/2021	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above						(September 2019)			
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
161	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA	01/2018	607.00 -	607.00	120.17	- -	08/2021	-	0/1
162	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	614.48	31.00	- -	08/2021	-	0/0
163	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	564.66	21.00	- -	08/2021	-	0/0
164	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 2,190.00	2,400.00	1,555.77	- 05/2019	11/2021	30(R3)	0/0
165	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 1,684.93	1,117.84	-	- 12/2018	12/2021	36(R3)	0/0
166	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 1,444.25	972.77	-	- 02/2019	02/2022	36(R3)	0/0
167	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 2,283.50	2,450.00	793.30	- 10/2019	-	-	0/0
168	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT	03/2018	1,161.39 1,404.00	1,161.39	-	- 11/2021	-	-	0/0
169	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH	01/2018	960.24 -	960.24	328.34	- -	08/2020	-	0/0
<u>National Highways Development Project</u>									
170	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	390.51	191.77	- -	03/2020	-	0/0
<u>Public Works Dept Of State</u>									
171	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	766.36	666.72	- 09/2019	-	-	0/0
172	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	847.02	1,086.49	- 09/2019	-	-	0/0
173	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	904.82	722.92	- 12/2019	-	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (September 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	Total		86,584.48	87,908.17	31,386.98				11/35
			-						
	<u>URBAN DEVELOPMENT</u>								
	<u>Central Public Works Department</u>								
174	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00	422.00	14.20	-	12/2020	-	0/0
			-			-			
175	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00	392.00	12.56	-	03/2021	7(R3)	0/0
			-			08/2020			
176	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU	11/2017	348.77	348.77	14.52	-	11/2021	-	0/0
			-			-			
	Total		1,162.77	1,162.77	41.28				0/0
			-						
	Grand Total		1,21,477.52	1,41,326.97	47,514.59				28/102

Details of Projects Without Milestones w.r.t. Original Schedule

Annexure - X

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
	<u>Airport Authority Of India Limited</u>					
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI,TRIPURA	09/2015	338.93 -	06/2019 -	12/2019	0/0
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,A & N ISLANDS	10/2013	314.61 -	09/2018 -	06/2020	0/0
3	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN - [N04000085]AAI,UTTARAKHAND	07/2018	353.27 -	09/2020 -	09/2020	0/0
4	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076]AAI,DELHI	11/2016	233.38 -	04/2020 -	12/2020	0/0
5	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA - [N04000080]AAI,WEST BENGAL	01/2016	219.91 -	03/2020 -	12/2020	0/0
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]AAI,ASSAM	12/2016	859.86 -	03/2021 -	03/2021	0/0
7	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT - [N04000079]AAI,MAHARASHTRA	03/2017	358.89 -	04/2021 -	04/2021	0/0
8	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]AAI,UTTAR PRADESH	06/2018	1,383.00 -	09/2021 -	09/2021	0/0
9	CONSTRUCTION OF TERMINAL BUILDING & ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]AAI,JAMMU AND KASHMIR	07/2018	323.19 -	09/2021 -	09/2021	0/0
10	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]AAI,TAMIL NADU	08/2018	951.28 -	10/2021 -	10/2021	0/0
11	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA - [N04000081]AAI,WEST BENGAL	01/2019	264.99 -	11/2021 -	11/2021	0/0
12	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI - [N04000074]AAI,TAMIL NADU	06/2018	2,467.00 -	02/2022 -	08/2022	0/0
13	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082]AAI,BIHAR	05/2018	539.20 -	10/2022 -	10/2022	0/0
	<u>COAL</u>					
	<u>Neyveli Lignite Corporation</u>					
14	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH	07/2016	17,237.00 -	11/2021 -	11/2021	0/0
15	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN	03/2015	522.45 -	09/2019 -	-	0/0
16	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN	03/2015	513.63 -	12/2019 -	-	0/0
	<u>Western Coal Fields Limited</u>					
17	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL,MAHARASHTRA	03/2017	362.73 -	03/2020 -	03/2020	0/0
18	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL,MADHYA PRADESH	07/2016	409.87 -	03/2022 -	03/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>INFORMATION AND BROADCASTING</u>					
	<u>Central Public Works Department</u>					
19	FILM AND TELEVISION INSTITUTE ARUNACHAL PRADESH - [N09000002]CPWD,ANDHRA PRADESH	11/2016	204.32 -	02/2019 -	11/2019	0/0
	<u>National Building Construcion Corporation Ltd</u>					
20	NATIONAL CENTRE OF EXCELLENCE FOR ANIMATION VISUAL EFFECTS GAMING AND COMICS - [N09000003]NBCC,MAHARASHTRA	12/2016	167.70 -	03/2020 -	03/2020	0/0
	<u>National Film Archive Of India</u>					
21	NATIONAL FILM HERITAGE MISSION - [N09000001]NFAI,MAHARASHTRA	11/2014	597.41 -	- -	-	0/0
	<u>PETROLEUM</u>					
	<u>Bharat Petroleum Corporation Limited</u>					
22	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]BPCL,KARNATAKA	10/2018	206.26 -	03/2021 -	03/2021	0/0
23	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 -	02/2017 -	10/2021	0/0
24	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL - [N16000365]BPCL,UTTAR PRADESH	12/2017	1,524.06 -	12/2021 -	12/2021	0/0
25	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA	12/2015	1,112.00 1,507.24	06/2019 02/2022	02/2022	0/0
26	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]BPCL,JHARKHAND	11/2018	248.55 -	06/2022 -	06/2022	0/0
27	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]BPCL,KERALA	09/2018	11,130.00 -	03/2023 -	03/2023	0/0
	<u>Chennai Petroleum Corporation Limited</u>					
28	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU	09/2017	1,858.00 -	12/2019 -	12/2019	0/0
29	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU	08/2017	421.00 -	08/2020 -	08/2020	0/0
	<u>Gas Authority Of India Limited</u>					
30	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA	02/2015	749.00 -	02/2020 -	02/2020	0/0
31	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL,ODISHA	07/2017	243.53 -	07/2022 -	07/2022	0/0
32	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]GAIL,ODISHA	07/2017	182.20 -	07/2022 -	07/2022	0/0
33	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]GAIL,BIHAR	10/2017	359.25 -	10/2022 -	10/2022	0/0
34	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR - [N16000330]GAIL,JHARKHAND	10/2017	221.45 -	10/2022 -	10/2022	0/0
	<u>Hindustan Petroleum Corporation Limited</u>					
35	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA	06/2017	249.26 -	06/2020 -	09/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
36	120 TMTA NEW LPG PLANT AT BARHI JHARKHAND STATE - [N16000316]HPCL,JHARKHAND	06/2017	161.50 -	06/2020 -	09/2021	0/0
37	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369]HPCL,KARNATAKA	12/2018	854.00 -	12/2022 -	12/2022	0/0
38	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR-CHAMPA IN STATE OF CHHATTISGARH - [N16000311]HPCL,CHHATTISGARH	12/2016	300.00 -	04/2021 -	-	0/0
	<u>Indian Oil Corporation Limited</u>					
39	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]IOCL,ANDHRA PRADESH	08/2017	384.58 -	04/2021 -	04/2020	0/0
40	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	06/2020 -	06/2020	0/0
41	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]IOCL,MADHYA PRADESH	08/2017	236.00 -	06/2020 -	08/2020	0/0
42	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL,WEST BENGAL	04/2016	1,021.00 -	12/2020 -	12/2020	0/0
43	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL,MAHARASHTRA	05/2016	261.00 -	01/2021 -	01/2021	0/0
44	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]IOCL,HARYANA	01/2019	909.00 -	01/2021 -	01/2021	0/0
45	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL,ANDHRA PRADESH	01/2015	342.00 -	03/2021 -	03/2021	0/0
46	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL,ANDHRA PRADESH	07/2014	247.00 -	03/2021 -	03/2021	0/0
47	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]IOCL,BIHAR	04/2018	522.00 -	03/2021 -	03/2021	0/0
48	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00 -	01/2021 -	04/2021	0/0
49	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH	08/2018	466.00 -	04/2021 -	07/2021	0/0
50	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	10/2020 -	08/2021	0/0
51	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]IOCL,ODISHA	11/2018	462.30 -	09/2021 -	09/2021	0/0
52	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 -	01/2021 -	10/2021	0/0
53	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]IOCL,ANDHRA PRADESH	10/2018	316.20 -	10/2021 -	10/2021	0/0
54	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	08/2021 -	11/2021	0/0
55	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA	12/2018	611.00 -	04/2022 -	04/2022	0/0
56	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]IOCL,ODISHA	06/2019	371.00 -	09/2022 -	09/2022	0/0
57	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	04/2022 -	02/2023	0/0
	<u>Indian Strategic Petroleum Reserves Ltd</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
58	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPL,KARNATAKA <u>Oil India Limited</u>	01/2006	993.00 -	01/2012 -	-	0/0
59	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM	07/2011	350.00 -	01/2019 -	09/2019	0/0
60	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN - [N16000356]OIL,ASSAM	06/2016	224.75 -	08/2020 -	08/2020	0/0
61	50MW WIND ENERGY POWER PROJECT - [N16000298]OIL,MULTI STATE	11/2015	500.00 -	06/2017 -	-	0/0
	<u>POWER</u>					
	<u>Chenab Valley Power Projects [P] Limited</u>					
62	KIRU HYDRO ELECTRIC PROJECT - [N18000278]CVPPPL,JAMMU AND KASHMIR <u>National Hydro-Electric Power Corporation</u>	03/2019	4,287.59 -	- -	-	0/0
63	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR	12/1999	578.62 -	06/2006 -	-	0/0
64	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH <u>National Thermal Power Corporation</u>	09/2003	6,285.33 -	09/2010 -	-	0/0
65	TALAI PALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH	09/2015	3,004.00 -	11/2019 -	11/2019	0/0
66	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC,ODISHA	05/2016	1,885.13 -	12/2018 -	03/2020	0/0
67	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC,WEST BENGAL	12/2016	529.68 -	11/2018 -	03/2020	0/0
68	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000273]NTPC,UTTAR PRADESH	12/2018	587.44 -	09/2020 -	09/2020	0/0
69	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000274]NTPC,UTTAR PRADESH	03/2019	349.00 -	11/2020 -	11/2020	0/0
70	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND <u>Power Grid Corporation Of India Limited</u>	10/2004	4,237.96 4,238.00	10/2017 -	-	0/0
71	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]PGCIL,MULTI STATE	03/2017	251.60 -	06/2019 -	06/2019	0/0
72	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL,RAJASTHAN	07/2016	1,429.38 -	01/2019 07/2019	09/2019	0/0
73	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE	05/2016	14,733.37 -	11/2019 -	11/2019	0/0
74	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA	04/2016	844.64 -	04/2019 -	11/2019	0/0
75	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE	09/2016	562.25 -	03/2019 -	11/2019	0/0
76	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE	03/2017	283.72 -	11/2019 -	11/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
77	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL, MULTI STATE	10/2016	608.24 -	04/2019 -	11/2019	0/0
78	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL, MULTI STATE	12/2015	3,654.00 -	04/2019 -	11/2019	0/0
79	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL, MULTI STATE	01/2014	374.63 -	04/2016 -	12/2019	0/0
80	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL, MULTI STATE	03/2015	197.40 -	03/2018 -	12/2019	0/0
81	GREEN ENERGY CORRIDORS - INTER STATE TRANSSMISSION SCHEME PART-D - [N18000218]PGCIL, MULTI STATE	05/2016	3,519.59 -	05/2019 -	12/2019	0/0
82	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL, MULTI STATE	10/2016	408.46 -	01/2019 -	12/2019	0/0
83	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL, MULTI STATE	02/2017	322.30 -	02/2019 -	12/2019	0/0
84	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL, MULTI STATE	03/2017	379.95 -	12/2019 -	12/2019	0/0
85	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL, MULTI STATE	03/2017	337.75 -	06/2019 -	12/2019	0/0
86	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL, GUJARAT	05/2017	175.64 -	09/2018 -	12/2019	0/0
87	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL, TAMIL NADU	05/2017	186.17 -	07/2019 -	12/2019	0/0
88	SUPPLEMENTARY TRANS. SYSTEM FOR UMSP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL, GUJARAT	12/2017	193.14 -	06/2019 -	12/2019	0/0
89	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL, WEST BENGAL	04/2016	454.11 -	04/2018 -	01/2020	0/0
90	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]PGCIL, MULTI STATE	02/2017	195.05 -	02/2020 -	02/2020	0/0
91	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL, MULTI STATE	08/2017	1,931.39 -	02/2020 -	02/2020	0/0
92	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL, MULTI STATE	09/2017	198.49 -	09/2019 -	02/2020	0/0
93	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL, MULTI STATE	03/2016	808.63 -	01/2018 -	03/2020	0/0
94	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL, MULTI STATE	02/2017	235.53 -	06/2019 -	03/2020	0/0
95	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL, KARNATAKA	05/2017	445.89 -	02/2019 -	03/2020	0/0
96	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL, MULTI STATE	02/2017	5,070.13 -	04/2020 -	04/2020	0/0
97	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL, MULTI STATE	11/2017	358.83 -	05/2020 -	05/2020	0/0
98	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL, MULTI STATE	03/2017	3,500.00 3,500.00	07/2020 -	07/2020	0/0
99	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL, MULTI STATE	12/2014	4,754.42 -	12/2018 -	12/2020	0/0
100	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL, MULTI STATE	12/2014	5,111.33 -	12/2018 -	12/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	<u>Thdc India Limited</u>					
101	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH	03/2019	11,089.42 -	09/2023 -	09/2023	0/0
	<u>HEAVY INDUSTRY</u>					
	<u>Bharat Heavy Electricals Limited</u>					
102	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL,DELHI	08/2016	1,554.00 -	09/2019 -	09/2019	0/0
	<u>HEALTH AND FAMILY WELFARE</u>					
	<u>HII Infra Tech Services Limited</u>					
103	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	04/2020 -	06/2020	0/0
104	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	06/2020 -	08/2020	0/0
105	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 -	05/2021 -	10/2021	0/0
	<u>Hospital Services Consultancy Corporation</u>					
106	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	03/2019 -	10/2019	0/0
107	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH	03/2018	601.02 -	- -	02/2020	0/0
108	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA	03/2018	582.99 -	- -	02/2020	0/0
109	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC,WEST BENGAL	04/2018	651.99 -	- -	02/2020	0/0
110	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH	03/2018	268.84 -	- -	04/2020	0/0
111	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA	01/2018	249.01 -	- -	05/2020	0/0
	<u>Hospital Services Consultancy Corporation Ltd</u>					
112	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	05/2018 -	09/2019	0/0
113	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	03/2019 -	10/2019	0/0
114	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI	12/2017	156.56 -	- -	02/2020	0/0
115	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL	08/2017	355.15 -	03/2019 -	03/2020	0/0
116	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	10/2020	0/0
117	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	-	0/0
118	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL	08/2016	244.00 -	09/2018 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>National Building Construcion Corporation Ltd</u>					
119	AIIMS BILASPUR - [N21000028]NBCC,HIMACHAL PRADESH	04/2018	1,351.00 -	09/2021 -	09/2021	0/0
	<u>RAILWAYS</u>					
	<u>Central Railways</u>					
120	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 199.12	03/2019 12/2019	12/2019	0/0
121	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50 -	03/2021 -	03/2022	0/0
122	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89 -	03/2021 -	03/2022	0/0
123	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA	02/2015	3,627.47 3,627.00	03/2024 -	03/2022	0/0
124	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	3,168.29 -	03/2023 -	03/2023	0/0
125	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19 -	03/2022 -	03/2023	0/0
126	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,449.91 -	03/2023 -	03/2023	0/0
127	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA	02/2016	1,876.00 -	03/2023 -	03/2023	0/0
128	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02 -	03/2022 -	03/2024	0/0
129	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA	02/2016	9,968.00 -	03/2024 -	03/2024	0/0
130	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA	02/2016	2,425.00 -	03/2024 -	03/2024	0/0
131	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00 -	03/2024 -	03/2024	0/0
132	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 -	03/2022 -	03/2024	0/0
133	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 -	03/2023 -	03/2024	0/0
	<u>Container Corporation Of India</u>					
134	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00 -	03/2019 -	12/2019	0/0
135	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	03/2019 -	12/2019	0/0
136	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	03/2019 -	02/2020	0/0
137	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	03/2018 -	03/2020	0/0
138	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32 -	03/2019 -	03/2020	0/0
139	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	03/2019 -	12/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
140	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI, ANDHRA PRADESH	01/2013	387.70 -	03/2018 -	-	0/0
141	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI, CHHATISGARH	05/2014	207.00 -	03/2018 -	-	0/0
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>					
142	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC, MULTI STATE	11/2007	16,592.00 51,101.00	03/2020 -	03/2020	0/0
143	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC, MULTI STATE	10/2006	11,589.00 30,357.00	- -	-	0/0
	<u>East Central Railways</u>					
144	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR, BIHAR	04/1998	180.82 726.31	- -	10/2019	0/0
145	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR, UTTAR PRADESH	08/2015	528.57 -	03/2019 -	12/2019	0/0
146	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR, BIHAR	04/2013	213.01 367.17	- -	01/2020	0/0
147	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]ECR, BIHAR	04/1997	324.73 898.53	03/2012 -	03/2020	0/0
148	KOSI BRIDGE (NL), ECR - [220100304]ECR, BIHAR	04/2002	499.41 516.02	03/2020 -	03/2020	0/0
149	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR, BIHAR	04/1996	477.88 751.55	03/2012 -	03/2020	0/0
150	GARHWA ROAD-RAMNA - [N22000465]ECR, JHARKHAND	03/2015	348.23 -	03/2021 -	12/2020	0/0
151	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR, JHARKHAND	03/1999	1,033.07 3,020.95	- -	03/2021	0/0
152	KODERMA-TILAIYA (NL), ECR - [220100305]ECR, JHARKHAND	04/2002	459.91 1,625.87	- -	03/2021	0/0
153	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR, BIHAR	04/1999	325.00 735.20	- -	03/2021	0/0
154	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR, BIHAR	04/2004	372.14 1,470.50	- -	03/2021	0/0
155	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR, UTTAR PRADESH	08/2015	2,436.21 -	03/2020 -	03/2021	0/0
156	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]ECR, BIHAR	04/1991	329.39 803.11	- -	12/2021	0/0
157	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR, BIHAR	04/1997	162.87 614.45	- -	03/2022	0/0
158	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR, BIHAR	04/2006	378.56 -	- -	03/2022	0/0
159	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS (NEPAL) GC - [N22000181]ECR, BIHAR	04/2009	548.00 -	03/2020 -	03/2022	0/0
160	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR, BIHAR	04/2016	744.04 1,215.54	03/2021 -	03/2022	0/0
161	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]ECR, BIHAR	04/2016	731.64 1,185.73	03/2021 -	03/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
162	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 519.33	- -	02/2023	0/0
163	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 2,066.78	- -	03/2023	0/0
164	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	1,605.17 1,605.17	- 03/2023	03/2023	0/0
165	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	03/2024	0/0
166	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR	04/2008	326.20 -	- -	03/2024	0/0
167	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	03/2024	0/0
168	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-	0/0
169	CONSTRUCTION OF ROBS IN THE STATE OF BIHAR - [N22000344]ECR,BIHAR	07/2004	599.63 674.00	12/2007 -	-	0/0
170	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 546.71	07/2014 -	-	0/0
171	ARA-BHABHUA ROAD (NL) - [N22000166]ECR,BIHAR	04/2008	633.87 -	- -	03/2023	0/0
172	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR	04/2008	445.25 -	- -	03/2024	0/0
173	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE	04/2008	415.67 -	- -	03/2024	0/0
174	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	03/2024	0/0
175	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	03/2024	0/0
176	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	03/2024	0/0
177	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	03/2024	0/0
178	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	03/2024	0/0
	<u>East Coast Railway</u>					
179	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	03/2020 -	03/2021	0/0
180	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 -	02/2019 -	03/2022	0/0
181	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 -	03/2022 -	03/2022	0/0
182	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	11/2018 -	03/2022	0/0
183	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 -	12/2018 03/2022	03/2022	0/0
184	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 -	10/2020 03/2023	03/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
185	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 -	03/2022 -	03/2023	0/0
186	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 -	03/2009 -	06/2024	0/0
187	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	06/2021 -	06/2024	0/0
188	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 -	03/2022 -	03/2025	0/0
	<u>Eastern Railways</u>					
189	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	05/2019	0/0
190	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	03/2020	0/0
191	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	11/2018 -	03/2021	0/0
192	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	542.18 -	03/2020 -	03/2021	0/0
193	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	03/2021	0/0
194	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	09/2021	0/0
195	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	02/2013 -	03/2024	0/0
196	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	03/2024	0/0
197	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	03/2019 12/2009	03/2025	0/0
198	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	03/2006 -	03/2025	0/0
199	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	03/2025	0/0
200	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	03/2025	0/0
201	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	03/2022 -	03/2025	0/0
202	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR -CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	03/2016 -	03/2025	0/0
203	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.51 -	03/2017 -	03/2025	0/0
204	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	03/2025	0/0
205	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	03/2016 -	03/2025	0/0
206	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	03/2017 -	03/2025	0/0
207	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	03/2025	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
208	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	03/2025	0/0
209	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	03/2005 -	03/2025	0/0
210	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	03/2025	0/0
211	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	03/2025	0/0
212	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96 -	02/2012 -	03/2025	0/0
213	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2025	0/0
214	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	03/2025	0/0
215	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	03/2017 -	03/2026	0/0
<u>Indian Railway Construction Company Limited</u>						
216	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA	04/2016	5,200.00 -	03/2020 -	06/2023	0/0
<u>Kolkata Metro Rail Corporation Limited</u>						
217	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-	0/0
<u>Metropolitan Rapid Transport Projects</u>						
218	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 1,781.98	03/2004 -	03/2021	0/0
219	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 918.53	03/2014 03/2021	03/2021	0/0
220	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	06/2021	0/0
221	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSHUPUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	03/2025	0/0
222	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-	0/0
223	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	04/2016 -	-	0/0
<u>North Central Railway</u>						
224	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH	03/2018	4,329.53 -	03/2023 -	03/2023	0/0
225	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-	0/0
226	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	2,030.50 -	- -	-	0/0
<u>North East Frontier Railway</u>						
227	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR, WEST BENGAL	04/1983	297.32 -	03/2019 -	03/2020	0/0
228	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	4,454.17 13,809.00	03/2011 -	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
229	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	385.20 1,532.00	03/2019 -	03/2020	0/0
230	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR, BIHAR	09/2006	532.87 2,145.00	03/2019 -	03/2020	0/0
231	DIMAPUR-TIZIT NL - [N22000196]NFR, NAGALAND	04/2013	4,274.00 -	03/2020 -	03/2020	0/0
232	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR, MULTI STATE	04/2010	242.22 -	03/2020 -	03/2020	0/0
233	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR, MULTI STATE	04/2011	414.84 -	03/2020 -	03/2020	0/0
234	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR, ASSAM	04/2011	314.00 728.00	03/2019 -	03/2020	0/0
235	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR, ASSAM	04/2015	2,232.32 -	03/2022 -	03/2020	0/0
236	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR, WEST BENGAL	04/2016	602.27 -	12/2021 -	03/2020	0/0
237	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	1,180.19 3,300.00	12/2008 -	03/2021	0/0
238	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR, MEGHALAYA	04/2010	906.46 -	03/2021 -	03/2021	0/0
239	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR, MULTI STATE	04/2010	241.52 -	- -	03/2021	0/0
240	DIGARU-HOJAI (102 KM) - [N22000389]NFR, ASSAM	04/2015	870.96 -	03/2021 -	03/2021	0/0
241	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND	04/2006	2,326.52 -	03/2015 -	10/2021	0/0
242	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	2,393.47 4,968.00	03/2014 03/2022	03/2022	0/0
243	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR, BIHAR	04/2008	333.76 -	- 03/2022	03/2022	0/0
244	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 -	- 03/2022	03/2022	0/0
245	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48 -	12/2015 -	-	0/0
246	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR, MULTI STATE	04/2013	1,798.00 -	03/2019 -	-	0/0
247	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR, MULTI STATE	04/1999	819.23 -	- -	-	0/0
248	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHOWA-JAIN - [N22000499]NFR, WEST BENGAL	02/1999	380.60 -	04/2010 -	-	0/0
<u>North Eastern Railway</u>						
249	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER, UTTAR PRADESH	03/2015	1,295.42 -	03/2022 -	12/2019	0/0
250	CHHAPRA-BALLIA UP - [N22000134]NER, MULTI STATE	03/2013	295.00 -	01/2019 -	01/2020	0/0
251	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER, UTTAR PRADESH	04/2017	622.50 427.00	04/2017 -	01/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
252	INDARA - DOHRGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	04/2016 -	06/2020	0/0
253	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	12/2019 -	04/2021	0/0
254	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	12/2021 -	12/2021	0/0
255	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH	04/2016	1,900.00 -	01/2022 -	01/2022	0/0
256	AUNRIHAR - JAUNPUR PATCH DOUBLING. - [N22000469]NER,UTTAR PRADESH	04/2016	600.00 -	01/2022 -	01/2022	0/0
257	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	04/2017 -	04/2022	0/0
258	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	04/2017 -	10/2022	0/0
259	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	12/2022 -	12/2022	0/0
260	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-	0/0
261	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0
262	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
263	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-	0/0
264	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-	0/0
265	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH	04/2016	602.50 -	- -	-	0/0
<u>North Western Railway</u>						
266	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	10/2018 -	10/2019	0/0
267	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	11/2019 -	05/2020	0/0
268	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 281.03	02/2019 -	05/2020	0/0
269	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	12/2019 -	06/2020	0/0
270	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	420.18 -	03/2020 -	06/2020	0/0
271	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 780.98	02/2019 -	03/2021	0/0
272	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	03/2020 -	04/2022	0/0
273	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	08/2022 -	09/2022	0/0
274	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
275	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-	0/0
	<u>Northern Railway</u>					
276	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	06/2020	0/0
277	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	12/2011 -	03/2021	0/0
278	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 -	03/2016 -	03/2021	0/0
279	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	03/2022	0/0
280	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	11/2002 -	06/2022	0/0
281	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	03/2023	0/0
282	UNCHAHAAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	1,229.00 -	- -	03/2023	0/0
283	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE	04/2007	328.14 -	03/2023 -	03/2023	0/0
284	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	03/2024	0/0
285	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	03/2024	0/0
286	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	03/2024	0/0
	<u>National High Speed Rail Corporation Limited</u>					
287	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE	12/2015	1,08,000.00 -	12/2023 12/2023	12/2023	0/0
	<u>Rail India Technical And Economic Service</u>					
288	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498]RITES,CHHATISGARH	02/2016	393.98 -	03/2020 -	03/2020	0/0
289	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-	0/0
	<u>Rail Vikas Nigam Ltd.</u>					
290	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	1,185.64 -	12/2017 -	03/2020	0/0
291	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	03/2019 -	03/2020	0/0
292	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	713.48 -	03/2020 -	03/2020	0/0
293	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	1,402.02 -	03/2020 -	06/2020	0/0
294	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	03/2016 -	12/2020	0/0
295	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT	04/2012	644.38 -	03/2021 -	03/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
296	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL, ODISHA	03/2006	948.04 -	03/2020 -	03/2021	0/0
297	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL, MADHYA PRADESH	04/2011	1,485.85 -	12/2020 -	03/2021	0/0
298	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA	04/1998	1,202.70 -	02/2015 -	12/2021	0/0
299	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL, GUJARAT	04/2012	975.62 -	12/2021 -	12/2021	0/0
300	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL, GUJARAT	04/2013	1,548.66 -	12/2021 -	03/2022	0/0
301	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL, ANDHRA PRADESH	03/2012	1,503.71 -	03/2020 -	03/2022	0/0
302	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL, ODISHA	03/2009	942.95 -	03/2019 -	06/2022	0/0
303	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL, UTTAR PRADESH	03/2012	1,183.25 -	12/2020 -	12/2022	0/0
304	VIJAYAWADA-GUDUR - [N22000369]RVNL, ANDHRA PRADESH	04/2015	3,246.26 -	12/2023 -	12/2023	0/0
305	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL, UTTAR PRADESH	04/2015	943.60 -	03/2022 -	12/2024	0/0
306	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL, TELANGANA	04/2015	773.94 -	12/2024 -	12/2024	0/0
307	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL, UTTAR PRADESH	04/2015	1,765.92 -	03/2023 -	12/2024	0/0
308	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL, ODISHA	01/1991	2,335.67 -	12/2024 -	12/2024	0/0
309	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	03/2016 -	03/2025	0/0
310	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	03/2016 -	03/2025	0/0
311	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL, UTTARAKHAND	04/2011	16,216.00 -	12/2024 -	03/2025	0/0
312	DIGHI PORT NEW LINE - [N22000408]RVNL, MAHARASHTRA	04/2015	723.78 -	12/2025 -	03/2025	0/0
313	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	12/2025	0/0
314	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL, HIMACHAL PRADESH	04/2008	2,966.99 -	12/2026 -	12/2025	0/0
<u>Railway Electrification</u>						
315	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE, UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-	0/0
<u>South Central Railway</u>						
316	MUNEERABAD-MAHABOBNAGAR(NL), SCR - [220100205]SCR, MULTI STATE	04/1997	1,723.00 1.00	03/2000 -	03/2021	0/0
317	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR, TELANGANA	04/2017	119.73 185.00	03/2022 -	03/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
318	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 -	03/2009 -	03/2023	0/0
319	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	03/2021 -	03/2023	0/0
320	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	03/2022 -	03/2023	0/0
321	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 -	03/2023 -	03/2024	0/0
322	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	164.36 -	02/2009 -	-	0/0
323	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	458.25 -	- -	-	0/0
324	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	761.37 -	- -	-	0/0
325	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-	0/0
<u>South East Central Railway</u>						
326	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- -	10/2019	0/0
327	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR,CHHATISGARH	04/2008	872.00 1,226.51	12/2019 10/2019	10/2019	0/0
328	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH	04/2015	1,370.00 1,370.00	12/2021 12/2021	12/2021	0/0
<u>South Eastern Railway</u>						
329	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	12/2016 08/2018	12/2019	0/0
330	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 358.68	12/2018 12/2018	06/2020	0/0
331	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 1,312.96	03/2020 -	06/2020	0/0
332	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	03/2021 -	12/2021	0/0
333	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- 03/2025	03/2025	0/0
334	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 -	03/2003 03/2030	03/2030	0/0
335	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	651.00 -	03/2015 -	-	0/0
336	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-	0/0
337	CONSTRUCTION OF ROBS IN THE STATE OF BIHAR (NEW ROBS-12) - [N22000337]SER,BIHAR	08/2010	400.00 -	03/2014 -	-	0/0
338	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-	0/0
<u>South Western Railway</u>						
339	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	03/2020 -	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
340	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 -	03/2017 -	03/2020	0/0
341	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 -	03/2019 -	03/2021	0/0
342	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01 -	- -	12/2023	0/0
343	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	12/2023	0/0
344	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	12/2023	0/0
345	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	348.85 -	- -	12/2023	0/0
346	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	12/2023	0/0
347	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	12/2023	0/0
348	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 -	03/2016 -	12/2023	0/0
349	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 -	03/2002 -	03/2024	0/0
350	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	03/2016 -	03/2024	0/0
351	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00 -	- -	12/2024	0/0
352	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 -	12/2018 -	12/2024	0/0
	<u>Southern Railway</u>					
353	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	03/2019 -	12/2019	0/0
354	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	02/2019 -	02/2020	0/0
355	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	03/2020	0/0
356	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	931.98 -	- -	03/2020	0/0
357	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU	10/2013	187.26 -	04/2014 -	03/2020	0/0
358	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	03/2020 -	03/2021	0/0
359	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU	02/2015	760.00 -	03/2020 -	06/2021	0/0
360	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU	02/2015	1,700.00 -	03/2022 -	03/2022	0/0
361	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	03/2024 -	03/2026	0/0
362	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	1,566.00 2,815.62	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
363	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	227.40 -	- -	-	0/0
364	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	- -	-	0/0
365	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	151.84 -	02/2019 -	-	0/0
366	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-	0/0
367	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-	0/0
368	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-	0/0
369	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 457.08	- -	-	0/0
370	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 252.96	- -	-	0/0
371	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-	0/0
372	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 189.24	- -	-	0/0
373	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 1,431.90	- 06/2022	-	0/0
374	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 828.50	- -	-	0/0
375	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	03/2005 -	-	0/0
376	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-	0/0
377	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU	02/1999	257.00 257.00	03/2018 -	-	0/0
	<u>Western Railway</u>					
378	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 03/2017	03/2017	0/0
379	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT	02/1991	551.51 809.07	03/2019 03/2020	03/2020	0/0
380	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	829.74 1,215.34	03/2020 03/2021	03/2021	0/0
381	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	844.10 844.10	- 03/2021	03/2021	0/0
382	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 1,002.39	03/2021 03/2021	03/2021	0/0
383	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT	04/2017	691.84 663.29	03/2020 03/2021	03/2021	0/0
384	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH	04/2016	700.00 603.69	06/2020 06/2021	06/2021	0/0
385	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 321.62	03/2012 03/2022	03/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
386	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 1,347.26	03/2022 03/2022	03/2022	0/0
387	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 858.56	03/2019 03/2022	03/2022	0/0
388	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	1,037.15 1,037.15	03/2021 03/2022	03/2022	0/0
389	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	3,503.69 3,860.00	03/2022 03/2023	03/2023	0/0
390	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 1,640.04	03/2022 03/2023	03/2023	0/0
391	GANDHINAGAR REDEVELOPMENT OF STATION ALOGLWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT	03/2017	243.60 -	- -	-	0/0
392	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-	0/0
393	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-	0/0
394	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-	0/0
395	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 -	- -	-	0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
	<u>Ministry Of Road Transport And Highways</u>					
396	MAJALGAON TO KAIJ - [N24001036]MORTH,MAHARASHTRA	01/2017	413.99 -	07/2019 -	07/2019	0/0
397	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	09/2019	0/0
398	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]MORTH,UTTAR PRADESH	10/2013	445.89 653.00	03/2017 -	09/2019	0/0
399	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA	08/2013	171.96 172.00	06/2016 -	11/2019	0/0
400	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2-LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MORTH,UTTARAKHAND	11/2017	232.81 -	11/2019 -	11/2019	0/0
401	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MORTH,UTTARAKHAND	11/2017	283.51 -	11/2019 -	11/2019	0/0
402	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MORTH,UTTARAKHAND	11/2017	266.52 -	11/2019 -	11/2019	0/0
403	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MORTH,A & N ISLANDS	11/2017	237.80 -	11/2019 -	11/2019	0/0
404	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MORTH,A & N ISLANDS	11/2017	257.34 -	11/2019 -	11/2019	0/0
405	BHADGAON TO CHALISGAON - [N24001047]MORTH,MAHARASHTRA	01/2018	259.55 260.00	11/2019 -	11/2019	0/0
406	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA	03/2014	191.50 192.00	05/2016 -	12/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
407	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MORTH,UTTARAKHAND	12/2017	257.34 -	12/2019 -	12/2019	0/0
408	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MORTH,UTTARAKHAND	12/2017	200.34 -	12/2019 -	12/2019	0/0
409	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MORTH,UTTARAKHAND	12/2017	248.22 -	12/2019 -	12/2019	0/0
410	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MORTH,UTTARAKHAND	06/2017	282.08 -	06/2019 -	12/2019	0/0
411	KHAMGAON TO SHEGAON - [N24001009]MORTH,MAHARASHTRA	02/2017	203.21 203.00	05/2019 -	12/2019	0/0
412	NANDGAON TO MORSHI - [N24001014]MORTH,MAHARASHTRA	01/2017	385.87 386.00	06/2019 -	12/2019	0/0
413	MORSHI TO ACHALPUR - [N24001015]MORTH,MAHARASHTRA	01/2017	341.16 341.00	06/2019 -	12/2019	0/0
414	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MORTH,MAHARASHTRA	03/2018	249.29 -	12/2019 -	12/2019	0/0
415	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MORTH,MAHARASHTRA	03/2018	219.91 -	12/2019 -	12/2019	0/0
416	PUNE TO MALE VILLAGE - [N24001078]MORTH,MAHARASHTRA	03/2018	228.31 -	12/2019 -	12/2019	0/0
417	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MORTH,MAHARASHTRA	03/2018	256.15 -	12/2019 -	12/2019	0/0
418	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MORTH,MAHARASHTRA	03/2018	223.46 -	12/2019 -	12/2019	0/0
419	JALGAON TO NANDURA - [N24001088]MORTH,MAHARASHTRA	03/2018	177.84 177.00	12/2019 -	12/2019	0/0
420	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]MORTH,MAHARASHTRA	03/2016	536.65 356.00	12/2019 -	12/2019	0/0
421	ARNI TO NAIGAINBANDI - [N24001093]MORTH,MAHARASHTRA	12/2017	309.94 310.00	12/2019 -	12/2019	0/0
422	NAIGAONBANDI TO MANGRULPIR - [N24001094]MORTH,MAHARASHTRA	12/2017	244.04 244.00	03/2019 -	12/2019	0/0
423	TALEGAON TO GONAPUR - [N24001096]MORTH,MAHARASHTRA	01/2018	264.41 264.00	03/2019 -	12/2019	0/0
424	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MORTH,UTTARAKHAND	08/2016	234.88 -	12/2017 -	12/2019	0/0
425	RISOD TO HINGOLI - [N24001149]MORTH,MAHARASHTRA	02/2018	355.99 355.99	12/2019 -	12/2019	0/0
426	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MORTH,UTTARAKHAND	02/2018	418.88 -	02/2020 -	02/2020	0/0
427	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MORTH,UTTARAKHAND	05/2018	248.00 -	05/2020 -	05/2020	0/0
428	DIGRAS DARWAH KARANJA - [N24001013]MORTH,MAHARASHTRA	01/2017	391.06 391.00	06/2019 -	06/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
429	KOTHARI TO DHANORA - [N24001073]MORTH,MAHARASHTRA	09/2018	301.38 301.00	08/2020 -	08/2020	0/0
430	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]MORTH,MADHYA PRADESH	01/2019	264.50 -	03/2021 -	03/2021	0/0
431	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA	10/2015	289.60 -	- -	-	0/0
432	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-	0/0
433	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-	0/0
434	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-	0/0
435	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-	0/0
436	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-	0/0
437	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-	0/0
438	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 -	08/2015 -	-	0/0
439	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-	0/0
440	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-	0/0
441	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-	0/0
442	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-	0/0
443	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-	0/0
444	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	11/2015 -	-	0/0
445	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA	01/1991	219.40 -	01/2018 -	-	0/0
446	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA	01/1991	218.63 -	10/2017 -	-	0/0
447	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-	0/0
448	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH,WEST BENGAL	01/1991	322.00 -	03/2018 -	-	0/0
449	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR	01/1991	282.41 -	08/2016 -	-	0/0
450	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR	01/1991	358.22 -	10/2016 -	-	0/0
451	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA	01/1991	229.41 -	05/2018 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
452	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-	0/0
453	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98 -	- -	-	0/0
454	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-	0/0
455	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-	0/0
456	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR	10/2013	278.39 -	08/2014 -	-	0/0
457	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR	11/2013	683.83 -	07/2016 -	-	0/0
458	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR	02/2014	665.50 -	07/2016 -	-	0/0
459	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR	02/2016	178.85 -	05/2016 -	-	0/0
460	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR	02/2016	369.77 -	06/2016 -	-	0/0
461	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR	02/2016	553.30 -	05/2016 -	-	0/0
462	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-	0/0
463	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPR - [N24000580]MORTH,BIHAR	03/2015	206.80 -	07/2016 -	-	0/0
464	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR	08/2015	288.24 -	11/2015 -	-	0/0
465	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR	08/2016	1,742.01 -	12/2016 -	-	0/0
466	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MORTH,ODISHA	01/2015	326.63 327.00	04/2018 -	-	0/0
467	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA	02/2015	239.91 240.00	10/2017 -	-	0/0
468	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA	07/2014	342.05 342.00	01/2017 -	-	0/0
469	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA	06/2016	157.30 157.00	06/2018 -	-	0/0
470	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MORTH,UTTARAKHAND	02/2018	293.68 -	- -	-	0/0
471	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MORTH,UTTARAKHAND	03/2018	460.73 -	- -	-	0/0
472	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26 - [N24000911]MORTH,ODISHA	03/2016	165.06 -	12/2016 -	-	0/0
473	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MORTH,ODISHA	08/2016	287.70 -	02/2017 -	-	0/0
474	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MORTH,ODISHA	09/2016	295.67 -	02/2017 -	-	0/0
475	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MORTH,ODISHA	12/2016	223.50 -	08/2018 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
476	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MORTH,ODISHA	12/2016	206.88 -	04/2018 -	-	0/0
477	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MORTH,ODISHA	03/2018	214.23 -	08/2018 -	-	0/0
478	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MORTH,ODISHA	03/2018	199.16 -	08/2018 -	-	0/0
479	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MORTH,BIHAR	09/2018	1,478.40 -	- -	-	0/0
480	MORSHI TO MAH/MP BORDER - [N24001016]MORTH,MAHARASHTRA	01/2017	471.61 472.00	06/2019 -	-	0/0
481	BHANDARA TO GHOTITOK - [N24001018]MORTH,MAHARASHTRA	01/2017	392.83 393.00	06/2019 -	-	0/0
482	MEHKAR TO AJISPUR - [N24001048]MORTH,MAHARASHTRA	01/2017	232.77 -	07/2019 -	-	0/0
483	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MORTH,MAHARASHTRA	02/2017	422.02 422.00	07/2019 -	-	0/0
484	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MORTH,MAHARASHTRA	01/2017	388.44 -	- -	-	0/0
485	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MORTH,MAHARASHTRA	02/2017	406.51 -	06/2019 -	-	0/0
486	WAKED TO TALEGAON - [N24001135]MORTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	-	0/0
487	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MORTH,ARUNACHAL PRADESH	09/2011	1,979.00 -	- -	-	0/0
488	ALWAR-NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MORTH,RAJASTHAN	03/2019	178.13 -	- -	-	0/0
<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
489	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL,ARUNACHAL PRADESH	10/2015	210.50 210.50	- 01/2016	01/2019	0/0
490	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM	04/2017	519.09 -	09/2019 -	09/2019	0/0
491	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM	04/2017	640.07 -	09/2019 -	09/2019	0/0
492	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM	04/2017	642.96 -	09/2019 -	09/2019	0/0
493	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM	04/2017	473.18 -	09/2019 -	09/2019	0/0
494	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM	04/2017	537.82 -	09/2019 -	09/2019	0/0
495	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM	04/2017	518.53 -	09/2019 -	09/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
496	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM	04/2017	404.29 -	09/2019 -	09/2019	0/0
497	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM	04/2017	428.11 -	09/2019 -	09/2019	0/0
498	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8 - [N24001184]NHIDCL,DELHI	07/2017	269.69 -	09/2019 -	12/2019	0/0
499	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D - [N24000974]NHIDCL,ARUNACHAL PRADESH	02/2017	199.02 199.02	- 02/2018	02/2021	0/0
500	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D - [N24000975]NHIDCL,ARUNACHAL PRADESH	02/2017	184.88 184.88	- 02/2018	02/2021	0/0
501	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH	02/2017	175.06 175.06	- 04/2019	04/2022	0/0
502	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL,ARUNACHAL PRADESH	02/2017	176.12 176.12	- 04/2019	04/2022	0/0
503	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND	03/2018	500.09 -	09/2018 -	-	0/0
504	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND	03/2018	339.57 233.35	09/2018 07/2019	-	0/0
505	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND	03/2018	272.89 -	09/2018 -	-	0/0
506	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND	03/2018	323.98 -	09/2018 -	-	0/0
507	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM	03/2017	375.80 -	- -	-	0/0
508	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITTA AND PANITNAKI I - [N24000770]NHIDCL,WEST BENGAL	03/2017	158.65 -	06/2018 -	-	0/0
509	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR	03/2018	253.44 -	07/2019 -	-	0/0
510	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA	03/2019	306.28 -	05/2019 -	-	0/0
511	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH	12/2016	200.44 -	- -	-	0/0
512	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH	03/2017	1,718.59 -	- -	-	0/0
513	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 37.500 TO KM - [N24000947]NHIDCL,ARUNACHAL PRADESH	05/2016	259.52 -	- -	-	0/0
514	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH	09/2016	568.92 -	- -	-	0/0
515	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH	12/2016	188.78 -	- -	-	0/0
516	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL,ASSAM	03/2017	1,049.51 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	National Highways Authority Of India					
517	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 -	03/2019 -	07/2019	0/0
518	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI, GUJARAT	05/2016	723.64 -	- -	09/2019	0/0
519	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI, GUJARAT	12/2016	417.19 -	- -	09/2019	0/0
520	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA	03/2017	639.79 -	03/2020 -	09/2019	0/0
521	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]NHAI,JHARKHAND	03/2017	165.50 -	03/2020 -	09/2019	0/0
522	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 255.23	11/2008 01/2011	08/2013	0/0
523	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 408.77	11/2008 07/2011	01/2014	0/0
524	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- 06/2015	06/2015	0/0
525	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- 06/2015	06/2015	0/0
526	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 03/2018	03/2018	0/0
527	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	04/2018 08/2018	08/2018	0/0
528	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 655.17	07/2009 10/2018	10/2018	0/0
529	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA	09/2016	1,004.67 -	05/2019 -	02/2019	0/0
530	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 -	03/2019	0/0
531	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 315.00	- 03/2020	03/2019	0/0
532	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 -	06/2019	0/0
533	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	02/2019 -	06/2019	0/0
534	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 456.92	02/2009 07/2019	07/2019	0/0
535	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	04/2010 -	07/2019	0/0
536	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	11/2017 -	07/2019	0/0
537	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 340.14	04/2009 03/2011	08/2019	0/0
538	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH	08/2016	227.49 -	01/2019 -	08/2019	0/0
539	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 1,544.00	09/2016 -	09/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
540	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 507.70	06/2016 -	09/2019	0/0
541	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 1,240.03	06/2019 12/2016	09/2019	0/0
542	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	06/2019 -	09/2019	0/0
543	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	06/2019 -	09/2019	0/0
544	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 2,525.80	09/2019 03/2020	09/2019	0/0
545	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 767.03	08/2018 -	09/2019	0/0
546	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	09/2019	0/0
547	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA	03/2017	296.19 -	03/2020 -	09/2019	0/0
548	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 -	10/2019	0/0
549	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	10/2019	0/0
550	TWO LANING WITH PAVED SHOULDER OF KARAU - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 09/2014	10/2019	0/0
551	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 537.16	07/2018 -	10/2019	0/0
552	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	07/2017 -	10/2019	0/0
553	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- -	10/2019	0/0
554	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 622.00	- -	10/2019	0/0
555	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 622.00	- -	10/2019	0/0
556	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	05/2018 10/2019	10/2019	0/0
557	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	05/2018 03/2018	10/2019	0/0
558	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	04/2019 -	10/2019	0/0
559	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	- 02/2016	10/2019	0/0
560	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	04/2019 10/2019	10/2019	0/0
561	FOUR LANING OF TALAJA - MAHUA SECTION OF NH - 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT	05/2016	834.64 -	- -	10/2019	0/0
562	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	- -	11/2019	0/0
563	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN	06/2016	763.23 -	06/2019 -	11/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
564	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 881.00	- 05/2017	11/2019	0/0
565	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	04/2019 11/2019	11/2019	0/0
566	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	- -	11/2019	0/0
567	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]NHAI,ANDHRA PRADESH	03/2017	648.32 -	03/2020 -	11/2019	0/0
568	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN	04/2017	894.00 -	04/2020 -	11/2019	0/0
569	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH	06/2017	648.33 -	06/2017 -	11/2019	0/0
570	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	11/2019	0/0
571	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	- -	11/2019	0/0
572	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	12/2019	0/0
573	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	12/2019	0/0
574	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014 -	12/2019	0/0
575	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	12/2019	0/0
576	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	12/2019	0/0
577	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	12/2019	0/0
578	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 -	06/2018 -	12/2019	0/0
579	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 897.03	11/2018 07/2019	12/2019	0/0
580	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 746.43	12/2017 06/2020	12/2019	0/0
581	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	- -	12/2019	0/0
582	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 67.34	01/2018 12/2018	12/2019	0/0
583	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI,WEST BENGAL	03/2016	229.37 -	11/2018 -	12/2019	0/0
584	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	- -	12/2019	0/0
585	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS- WEST BENGAL BORDER SECTION OF NH- [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	- 12/2017	12/2019	0/0
586	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	05/2019 -	12/2019	0/0
587	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	- -	12/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
588	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	05/2019 -	12/2019	0/0
589	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	12/2019	0/0
590	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI,WEST BENGAL	10/2015	361.15 -	- -	01/2020	0/0
591	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	- -	01/2020	0/0
592	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	01/2020	0/0
593	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	01/2020	0/0
594	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	08/2018 -	01/2020	0/0
595	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	10/2017 -	01/2020	0/0
596	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB	03/2018	196.05 149.90	- -	01/2020	0/0
597	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	10/2013 -	02/2020	0/0
598	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	- -	02/2020	0/0
599	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	- -	02/2020	0/0
600	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	07/2018 12/2019	02/2020	0/0
601	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA	03/2017	247.02 -	03/2020 02/2021	02/2020	0/0
602	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	04/2008 -	03/2020	0/0
603	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	03/2020	0/0
604	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 2,967.50	11/2011 -	03/2020	0/0
605	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 1,302.98	03/2018 -	03/2020	0/0
606	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	- -	03/2020	0/0
607	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	08/2018 -	03/2020	0/0
608	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 598.13	04/2018 03/2020	03/2020	0/0
609	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	- -	03/2020	0/0
610	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	08/2018 -	03/2020	0/0
611	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 -	03/2020 -	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
612	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA	03/2017	744.64 -	03/2020 -	03/2020	0/0
613	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR	03/2017	672.89 -	03/2020 -	03/2020	0/0
614	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI,JHARKHAND	03/2017	239.68 -	03/2020 -	03/2020	0/0
615	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH	03/2017	2,064.99 -	03/2020 -	03/2020	0/0
616	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	- -	03/2020	0/0
617	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 3,207.63	- 02/2018	03/2020	0/0
618	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	- -	03/2020	0/0
619	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA	03/2018	275.12 -	- -	03/2020	0/0
620	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXIST - [N24000837]NHAI,HARYANA	03/2018	307.79 -	- -	03/2020	0/0
621	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA	03/2018	198.05 -	- -	03/2020	0/0
622	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA	03/2018	551.58 -	- -	03/2020	0/0
623	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	04/2020	0/0
624	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 2,257.49	07/2018 -	04/2020	0/0
625	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 3,007.86	06/2018 -	04/2020	0/0
626	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	04/2018 -	04/2020	0/0
627	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	- -	04/2020	0/0
628	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	06/2018 -	04/2020	0/0
629	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 1,367.00	- -	04/2020	0/0
630	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20 -	04/2020 -	04/2020	0/0
631	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	03/2020 -	04/2020	0/0
632	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270 (D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	05/2018 03/2019	05/2020	0/0
633	4-LANNING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	05/2020	0/0
634	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	07/2018 -	05/2020	0/0
635	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 911.07	02/2020 11/2017	05/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
636	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	03/2020 -	05/2020	0/0
637	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 2,602.09	03/2020 11/2017	05/2020	0/0
638	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	05/2020	0/0
639	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	07/2016 -	05/2020	0/0
640	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	06/2020	0/0
641	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	07/2014 -	06/2020	0/0
642	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 2,182.03	06/2018 -	06/2020	0/0
643	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 2,433.38	06/2018 -	06/2020	0/0
644	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	03/2020 -	06/2020	0/0
645	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	09/2017 -	06/2020	0/0
646	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA	03/2018	181.78 -	- -	06/2020	0/0
647	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 2,273.00	12/2018 12/2019	07/2020	0/0
648	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	04/2019 07/2020	07/2020	0/0
649	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	- -	07/2020	0/0
650	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	07/2020	0/0
651	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	03/2020 -	07/2020	0/0
652	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 -	08/2020	0/0
653	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	08/2020	0/0
654	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 01/2019	08/2020	0/0
655	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 870.00	03/2019 03/2017	08/2020	0/0
656	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE - - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	- -	08/2020	0/0
657	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	03/2020 -	08/2020	0/0
658	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	03/2020 -	08/2020	0/0
659	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT	06/2017	1,958.88 -	06/2020 -	08/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
660	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	09/2017 -	08/2020	0/0
661	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 12/2019	09/2020	0/0
662	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 09/2017	09/2020	0/0
663	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	05/2018 -	09/2020	0/0
664	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 2,170.44	- -	09/2020	0/0
665	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	08/2017 -	09/2020	0/0
666	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN	02/2018	1,103.88 -	- -	09/2020	0/0
667	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	- -	10/2020	0/0
668	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	- 10/2020	10/2020	0/0
669	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 448.18	- -	10/2020	0/0
670	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	03/2019 -	11/2020	0/0
671	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	03/2019 -	11/2020	0/0
672	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 1,071.00	03/2017 05/2018	11/2020	0/0
673	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	10/2017 -	11/2020	0/0
674	FOUR LANING OF CHETTICKULAM TO NATHAM SECTION OF NH-785 FROM CHETTICKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35 -	- -	11/2020	0/0
675	FOUR LANING OF MADURAI- CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICKULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	- -	11/2020	0/0
676	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53 -	- 11/2020	11/2020	0/0
677	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21 -	- -	11/2020	0/0
678	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	08/2016 -	12/2020	0/0
679	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	12/2020	0/0
680	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	07/2019 12/2020	12/2020	0/0
681	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	07/2019 12/2020	12/2020	0/0
682	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 1,008.00	08/2019 -	12/2020	0/0
683	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGPUR ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	- -	12/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
684	CONSTRUCTION OF SIX LANE OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43 -	- -	12/2020	0/0
685	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA	03/2018	1,484.30 -	- -	12/2020	0/0
686	FOUR LANE OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA	03/2018	642.13 -	- -	12/2020	0/0
687	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	- -	01/2021	0/0
688	FOUR LANE OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB	02/2018	261.76 -	- -	01/2021	0/0
689	SIX LANE OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT	02/2018	1,052.21 1,449.00	- -	01/2021	0/0
690	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT	03/2018	2,702.05 -	- -	01/2021	0/0
691	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	03/2019 -	02/2021	0/0
692	FOUR LANE OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26 -	- -	02/2021	0/0
693	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH	03/2018	565.09 -	- -	02/2021	0/0
694	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	08/2019 -	03/2021	0/0
695	4-LANNING OF KODEBAD-DHANTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	03/2019 -	03/2021	0/0
696	REHABILITATION AND UPGRADATION TO FOUR LANE OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	- -	03/2021	0/0
697	REHABILITATION AND UPGRADATION BY 4-LANE OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	03/2020 -	03/2021	0/0
698	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH	03/2018	1,029.96 -	- 03/2021	03/2021	0/0
699	4-LANE OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 1,073.10	- 03/2019	03/2021	0/0
700	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	03/2019 04/2021	04/2021	0/0
701	FOUR LANE OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANE WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU	03/2018	1,016.92 -	- -	04/2021	0/0
702	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA	03/2018	806.11 -	- -	04/2021	0/0
703	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	03/2020 -	05/2021	0/0
704	FOUR LANE OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH	03/2018	478.74 1,071.75	- -	05/2021	0/0
705	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	07/2017 11/2020	06/2021	0/0
706	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	- 07/2020	06/2021	0/0
707	REHABILITATION AND UPGRADATION OF FOUR LANE OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	- -	06/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
708	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	- 05/2020	06/2021	0/0
709	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	- 05/2020	06/2021	0/0
710	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	- 03/2020	06/2021	0/0
711	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	- -	06/2021	0/0
712	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	- -	07/2021	0/0
713	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 -	- -	07/2021	0/0
714	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 -	- -	07/2021	0/0
715	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64 1,687.00	- 12/2018	07/2021	0/0
716	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA	03/2018	634.70 931.21	- -	07/2021	0/0
717	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA	03/2018	795.50 -	- -	07/2021	0/0
718	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 -	- -	07/2021	0/0
719	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	- -	08/2021	0/0
720	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	- -	08/2021	0/0
721	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	06/2020 -	09/2021	0/0
722	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 2,190.00	- 05/2019	11/2021	0/0
723	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 1,684.93	- 12/2018	12/2021	0/0
724	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	08/2017 -	02/2022	0/0
725	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 1,444.25	- 02/2019	02/2022	0/0
726	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-	0/0
727	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 2,519.00	06/2015 -	-	0/0
728	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-	0/0
729	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	-	0/0
730	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	-	0/0
731	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
732	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT	01/2011	953.88 -	07/2013 -	-	0/0
733	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI, TAMIL NADU	05/2010	374.00 -	05/2013 -	-	0/0
734	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI, TAMIL NADU	09/2011	485.00 -	08/2013 -	-	0/0
735	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI, ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-	0/0
736	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, BIHAR	09/2011	574.00 -	03/2014 -	-	0/0
737	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, BIHAR	10/2011	375.09 -	04/2014 -	-	0/0
738	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, BIHAR	01/2011	575.00 -	07/2013 -	-	0/0
739	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI, BIHAR	05/2011	511.54 -	11/2013 -	-	0/0
740	PANIKHOLI-RIMOLI - [N24000197]NHAI, ODISHA	03/2012	1,410.00 -	09/2014 -	-	0/0
741	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI, UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	-	0/0
742	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH	07/2012	291.36 -	01/2014 -	-	0/0
743	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI, TAMIL NADU	04/2012	624.00 -	04/2014 -	-	0/0
744	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI, JHARKHAND	12/2012	1,479.00 -	06/2015 -	-	0/0
745	ETAWAH CHAKERI - [N24000219]NHAI, UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-	0/0
746	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI, MULTI STATE	10/2012	1,928.22 -	04/2015 -	-	0/0
747	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI, HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	-	0/0
748	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE - I - [N24000347]NHAI, HARYANA	08/2015	723.54 -	02/2018 -	-	0/0
749	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI, TAMIL NADU	07/2014	401.11 -	01/2017 -	-	0/0
750	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI, UTTAR PRADESH	04/2014	351.34 -	01/2016 -	-	0/0
751	VADODARA-SURAT SECTION - [N24000361]NHAI, GUJARAT	03/2014	503.16 -	08/2016 -	-	0/0
752	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI, UTTAR PRADESH	06/2014	301.04 -	01/2016 -	-	0/0
753	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI, UTTAR PRADESH	04/2014	495.78 -	01/2016 -	-	0/0
754	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI, MAHARASHTRA	07/2015	2,288.18 -	05/2019 -	-	0/0
755	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI, MAHARASHTRA	07/2015	1,885.74 -	05/2019 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
756	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	04/2018 -	-	0/0
757	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,MULTI STATE	09/2015	788.51 -	03/2018 -	-	0/0
758	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	04/2019 -	-	0/0
759	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH	09/2015	785.78 -	03/2018 -	-	0/0
760	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	01/2019 -	-	0/0
761	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-	0/0
762	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA	09/2005	168.00 -	06/2006 -	-	0/0
763	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-	0/0
764	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	-	0/0
765	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	04/2019 -	-	0/0
766	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA	11/2015	867.66 -	05/2018 -	-	0/0
767	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	-	0/0
768	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	-	0/0
769	FOUR LANING FROM MPMHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	-	0/0
770	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	- -	-	0/0
771	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	- -	-	0/0
772	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR	08/2015	516.13 -	04/2018 -	-	0/0
773	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-	0/0
774	MEERUT-BULANDSHAHR - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	- -	-	0/0
775	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR-HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 -	07/2018 -	-	0/0
776	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	04/2019 -	-	0/0
777	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	11/2018 -	-	0/0
778	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-	0/0
779	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
780	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI, GUJARAT	05/2016	998.18 -	- -	-	0/0
781	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI, GUJARAT	05/2016	763.08 -	- -	-	0/0
782	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI, GUJARAT	05/2016	425.60 241.41	- -	-	0/0
783	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI, BIHAR	05/2015	581.84 -	05/2017 -	-	0/0
784	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI, RAJASTHAN	07/2016	331.46 -	10/2018 -	-	0/0
785	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]NHAI, DELHI	09/2015	771.18 -	- -	-	0/0
786	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI, ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-	0/0
787	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI, UTTAR PRADESH	01/2017	450.68 -	- -	-	0/0
788	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI, MADHYA PRADESH	09/2017	374.40 -	09/2017 -	-	0/0
789	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI, MADHYA PRADESH	12/2017	950.27 -	- -	-	0/0
790	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI, BIHAR	12/2017	2,598.00 -	- -	-	0/0
791	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI, ANDHRA PRADESH	12/2017	357.00 -	- -	-	0/0
792	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI, UTTAR PRADESH	12/2017	207.00 -	- -	-	0/0
793	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI, UTTAR PRADESH	12/2017	305.00 -	- -	-	0/0
794	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI, BIHAR	01/2018	573.70 -	- -	-	0/0
795	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI, BIHAR	01/2018	895.39 -	- -	-	0/0
796	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI, JHARKHAND	01/2018	273.46 -	- -	-	0/0
797	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI, JHARKHAND	01/2018	1,155.16 -	- -	-	0/0
798	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI, MADHYA PRADESH	01/2018	770.73 -	- -	-	0/0
799	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI, ODISHA	01/2018	633.68 -	- -	-	0/0
800	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM - [N24000737]NHAI, ODISHA	01/2018	1,522.00 -	- -	-	0/0
801	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI, ODISHA	01/2018	999.00 -	- -	-	0/0
802	VARANASI RING ROAD PKG - I - [N24000740]NHAI, UTTAR PRADESH	01/2018	450.77 929.89	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
803	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA	03/2017	4,429.00 -	03/2017 -	-	0/0
804	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA	02/2018	486.78 -	- -	-	0/0
805	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 -	- -	-	0/0
806	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 -	- -	-	0/0
807	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 2,283.50	- 10/2019	-	0/0
808	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI,WEST BENGAL	03/2018	1,261.98 -	- -	-	0/0
809	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 -	- -	-	0/0
810	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH	03/2018	925.40 -	- -	-	0/0
811	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN	02/2018	741.86 -	- -	-	0/0
812	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN	02/2018	716.76 -	- -	-	0/0
813	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	-	0/0
814	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 -	- -	-	0/0
815	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH	03/2018	1,025.80 -	- -	-	0/0
816	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH	03/2018	1,115.28 -	- -	-	0/0
817	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K - [N24000804]NHAI,TELANGANA	03/2018	802.65 -	- -	-	0/0
818	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-	0/0
819	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	- -	-	0/0
820	FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA	03/2018	950.63 -	- -	-	0/0
821	FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA	03/2018	857.62 -	- -	-	0/0
822	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHTRA - [N24000825]NHAI,TELANGANA	03/2018	828.29 -	- -	-	0/0
823	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU	03/2018	633.55 -	- -	-	0/0
824	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU	03/2018	2,065.96 -	- -	-	0/0
825	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE	03/2018	1,294.47 -	- -	-	0/0
826	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE	03/2018	998.70 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
827	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI, GUJARAT	03/2018	1,161.39 1,404.00	- 11/2021	-	0/0
828	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI, RAJASTHAN	03/2018	874.25 -	- -	-	0/0
829	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI, RAJASTHAN	03/2018	1,158.35 -	- -	-	0/0
830	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI, PUNJAB	03/2018	199.90 149.90	- -	-	0/0
831	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH – 14 - [N24001185]NHAI, UTTAR PRADESH	11/2017	2,159.00 -	01/2019 -	-	0/0
832	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI, HARYANA	01/2019	1,051.91 -	- -	-	0/0
833	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI, HARYANA	01/2019	1,120.06 -	- -	-	0/0
834	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI, HARYANA	01/2019	1,137.42 -	- -	-	0/0
835	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI, HARYANA	01/2019	1,033.19 -	- -	-	0/0
836	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI, HARYANA	01/2019	1,243.45 -	- -	-	0/0
837	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI, HARYANA	01/2019	889.36 -	- -	-	0/0
838	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI, HARYANA	01/2019	1,018.79 -	- -	-	0/0
839	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI, HARYANA	01/2019	996.65 -	- -	-	0/0
840	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI, MADHYA PRADESH	10/2019	743.88 -	- -	-	0/0
841	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI, UTTAR PRADESH	05/2015	261.09 275.00	05/2017 -	-	0/0
842	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI, TAMIL NADU	06/2015	563.92 -	12/2017 -	-	0/0
843	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI, MADHYA PRADESH	01/2018	960.24 -	- -	08/2020	0/0
National Highways Development Project						
844	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP, UTTAR PRADESH	10/2013	445.89 -	03/2017 -	09/2019	0/0
845	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP, MADHYA PRADESH	01/2012	410.72 -	04/2015 -	10/2019	0/0
846	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP, MADHYA PRADESH	11/2015	628.45 -	01/2020 -	01/2020	0/0
847	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP, MADHYA PRADESH	12/2015	957.54 -	02/2020 -	02/2020	0/0
848	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP, MADHYA PRADESH	06/2015	390.51 -	- -	03/2020	0/0
849	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP, MADHYA PRADESH	11/2013	497.05 -	05/2017 -	05/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
850	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	- -	-	0/0
	Public Works Dept Of State					
851	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O - [N24000871]PWD, WEST BENGAL	08/2014	600.87 720.97	11/2017 05/2019	05/2019	0/0
852	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873]PWD, WEST BENGAL	08/2014	823.20 937.76	11/2017 06/2019	06/2019	0/0
853	REHABILITATION AND UPGADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]PWD, WEST BENGAL	04/2014	279.70 398.52	08/2017 07/2019	07/2019	0/0
854	REHABILITATION AND UPGADATION OF ALLAHABAD -MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2- - [N24001147]PWD, UTTAR PRADESH	10/2016	239.63 -	02/2019 -	07/2019	0/0
855	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 - [N24000962]PWD, MADHYA PRADESH	09/2016	178.23 -	09/2018 -	08/2019	0/0
856	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]PWD, TELANGANA	01/2017	359.27 -	05/2019 -	08/2019	0/0
857	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD, TELANGANA	03/2015	153.21 -	01/2017 -	09/2019	0/0
858	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD, ODISHA	12/2011	159.39 -	11/2017 -	09/2019	0/0
859	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]PWD, HARYANA	01/2017	247.25 -	03/2019 03/2020	09/2019	0/0
860	REHABILITATION AND UPGADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]PWD, UTTAR PRADESH	11/2016	215.16 215.00	09/2019 -	09/2019	0/0
861	REHABILITATION AND UPGADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO - [N24001143]PWD, UTTAR PRADESH	10/2016	176.94 177.00	10/2018 -	09/2019	0/0
862	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH - [N24001145]PWD, UTTAR PRADESH	05/2013	164.54 165.00	08/2015 -	09/2019	0/0
863	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]PWD, NAGALAND	11/2016	336.25 369.96	09/2019 -	09/2019	0/0
864	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]PWD, PUNJAB	10/2017	1,069.59 -	10/2019 -	10/2019	0/0
865	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]PWD, TELANGANA	01/2017	196.52 -	10/2019 -	10/2019	0/0
866	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]PWD, TELANGANA	01/2017	605.08 -	10/2019 -	10/2019	0/0
867	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C - [N24000999]PWD, BIHAR	11/2016	230.34 -	10/2019 -	10/2019	0/0
868	REHABILITATION AND UPGADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]PWD, UTTAR PRADESH	07/2016	208.88 -	10/2019 -	10/2019	0/0
869	R AND U FROM KM 385.00 TO KM 420.000 TO 2- LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404 - [N24001205]PWD, UTTAR PRADESH	12/2016	209.10 -	10/2019 -	10/2019	0/0
870	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]PWD, WEST BENGAL	03/2016	271.17 291.20	11/2018 11/2019	11/2019	0/0
871	REHABILITATION AND UPGADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]PWD, MADHYA PRADESH	11/2017	235.91 -	02/2018 -	11/2019	0/0
872	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879]PWD, WEST BENGAL	03/2017	202.69 202.69	11/2019 -	11/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
873	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]PWD,MADHYA PRADESH	11/2017	184.62 -	02/2018 -	11/2019	0/0
874	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884]PWD,MADHYA PRADESH	03/2018	191.21 -	11/2019 -	11/2019	0/0
875	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]PWD,MADHYA PRADESH	03/2018	214.69 -	03/2018 -	11/2019	0/0
876	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]PWD,MADHYA PRADESH	03/2018	233.04 -	03/2018 -	11/2019	0/0
877	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]PWD,MADHYA PRADESH	11/2017	254.17 -	02/2018 -	11/2019	0/0
878	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 - [N24000895]PWD,MADHYA PRADESH	09/2016	287.34 -	01/2019 -	11/2019	0/0
879	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]PWD,MADHYA PRADESH	03/2016	877.79 -	06/2019 -	11/2019	0/0
880	REHABILITATION AND UPGRADATION OF HARPALPUR -SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942]PWD,UTTAR PRADESH	03/2016	208.50 -	11/2019 -	11/2019	0/0
881	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]PWD,TELANGANA	02/2018	294.13 -	11/2019 -	11/2019	0/0
882	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]PWD,TELANGANA	02/2018	220.28 -	11/2019 -	11/2019	0/0
883	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]PWD,UTTAR PRADESH	03/2016	249.50 -	05/2019 -	11/2019	0/0
884	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]PWD,MADHYA PRADESH	11/2017	392.33 -	03/2018 -	11/2019	0/0
885	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA	01/2014	255.75 348.00	09/2017 -	12/2019	0/0
886	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	03/2011 -	12/2019	0/0
887	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	12/2019	0/0
888	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 240.58	08/2013 -	12/2019	0/0
889	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 269.14	02/2013 09/2017	12/2019	0/0
890	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	08/2015 -	12/2019	0/0
891	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]PWD,MADHYA PRADESH	03/2018	162.56 -	03/2018 -	12/2019	0/0
892	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]PWD,TELANGANA	10/2016	298.32 -	02/2019 -	12/2019	0/0
893	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]PWD,TELANGANA	10/2016	248.83 -	03/2019 -	12/2019	0/0
894	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]PWD,TELANGANA	01/2017	283.00 -	12/2019 -	12/2019	0/0
895	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]PWD,TELANGANA	01/2017	300.00 -	05/2019 -	12/2019	0/0
896	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]PWD,TELANGANA	01/2018	230.03 -	12/2019 -	12/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
897	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997]PWD,TELANGANA	03/2018	192.67 -	07/2019 -	12/2019	0/0
898	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM - [N24001153]PWD,ASSAM	11/2010	197.37 -	02/2014 -	12/2019	0/0
899	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]PWD,MIZORAM	08/2010	186.96 -	09/2014 -	12/2019	0/0
900	REHABILITATION AND UPGRADATION OF BARAICH -SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA - [N24001202]PWD,UTTAR PRADESH	03/2016	388.83 -	12/2019 -	12/2019	0/0
901	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]PWD,MADHYA PRADESH	11/2017	249.05 -	07/2018 -	01/2020	0/0
902	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]PWD,UTTAR PRADESH	03/2016	240.30 240.00	01/2020 -	01/2020	0/0
903	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148]PWD,UTTAR PRADESH	03/2016	599.34 -	01/2020 -	01/2020	0/0
904	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH	03/2015	511.83 -	08/2017 -	02/2020	0/0
905	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]PWD,MADHYA PRADESH	01/2016	809.16 -	07/2018 -	02/2020	0/0
906	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]PWD,UTTAR PRADESH	03/2018	185.18 -	02/2020 -	02/2020	0/0
907	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	954.43 -	09/2015 -	03/2020	0/0
908	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA - [N24001139]PWD,UTTAR PRADESH	10/2016	218.94 219.00	03/2020 -	03/2020	0/0
909	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203]PWD,UTTAR PRADESH	10/2016	218.90 -	03/2020 -	03/2020	0/0
910	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]PWD,MADHYA PRADESH	02/2018	279.44 -	03/2018 -	04/2020	0/0
911	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]PWD,TELANGANA	02/2018	426.52 -	04/2020 -	04/2020	0/0
912	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]PWD,UTTAR PRADESH	03/2018	263.89 -	04/2020 -	04/2020	0/0
913	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]PWD,MADHYA PRADESH	01/2017	373.82 -	09/2019 -	05/2020	0/0
914	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]PWD,TELANGANA	01/2018	283.15 -	05/2020 -	05/2020	0/0
915	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]PWD,KARNATAKA	05/2018	171.60 -	05/2018 -	05/2020	0/0
916	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	10/2010 -	06/2020	0/0
917	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]PWD,MADHYA PRADESH	03/2018	166.21 -	08/2018 -	06/2020	0/0
918	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]PWD,MADHYA PRADESH	01/2017	205.05 -	03/2017 -	06/2020	0/0
919	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]PWD,MADHYA PRADESH	03/2018	217.22 -	08/2018 -	06/2020	0/0
920	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906]PWD,PUNJAB	03/2018	173.24 -	06/2020 -	06/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
921	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]PWD,TELANGANA	02/2018	206.13 -	06/2020 -	06/2020	0/0
922	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131]PWD,JHARKHAND	03/2018	212.99 -	06/2020 -	06/2020	0/0
923	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]PWD,MADHYA PRADESH	02/2018	169.63 -	03/2018 -	07/2020	0/0
924	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905]PWD,PUNJAB	03/2018	322.48 -	07/2020 -	07/2020	0/0
925	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]PWD,TELANGANA	03/2018	626.76 -	07/2020 -	07/2020	0/0
926	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]PWD,PUNJAB	03/2018	293.10 -	08/2020 -	08/2020	0/0
927	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927]PWD,PUNJAB	03/2018	293.64 -	08/2020 -	08/2020	0/0
928	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]PWD,PUNJAB	03/2018	293.64 -	08/2020 -	08/2020	0/0
929	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]PWD,TRIPURA	10/2016	171.90 -	08/2020 -	08/2020	0/0
930	FOUR LANING WIDENING & STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (JAN - [N24001208]PWD,UTTAR PRADESH	03/2018	288.30 -	08/2020 -	08/2020	0/0
931	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]PWD,WEST BENGAL	02/2018	426.18 426.18	09/2020 -	09/2020	0/0
932	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]PWD,TELANGANA	03/2018	322.81 -	09/2020 -	09/2020	0/0
933	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]PWD,UTTAR PRADESH	03/2016	296.50 -	09/2020 -	09/2020	0/0
934	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883]PWD,WEST BENGAL	03/2018	254.30 254.30	10/2020 -	10/2020	0/0
935	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]PWD,WEST BENGAL	02/2018	218.70 218.70	11/2020 -	11/2020	0/0
936	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM KM MAKHU (DESIGN CH 0 000 - [N24000910]PWD,PUNJAB	03/2018	170.57 -	11/2020 -	11/2020	0/0
937	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. - [N24001174]PWD,MANIPUR	10/2016	235.31 -	11/2020 -	11/2020	0/0
938	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]PWD,NAGALAND	03/2017	217.35 -	11/2020 -	11/2020	0/0
939	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]PWD,BIHAR	05/2014	199.98 -	08/2016 -	12/2020	0/0
940	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]PWD,NAGALAND	10/2016	167.62 -	12/2020 -	12/2020	0/0
941	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]PWD,NAGALAND	10/2016	172.63 -	12/2020 -	12/2020	0/0
942	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION - [N24001173]PWD,KARNATAKA	02/2017	157.32 188.00	05/2019 -	05/2021	0/0
943	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197]PWD,GUJARAT	03/2018	351.00 -	06/2021 -	06/2021	0/0
944	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]PWD,WEST BENGAL	03/2016	160.27 213.97	08/2019 -	08/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
945	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]PWD, WEST BENGAL	06/2016	236.78 263.26	08/2019 -	08/2021	0/0
946	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152]PWD, ASSAM	09/2018	160.00 -	09/2021 -	09/2021	0/0
947	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180]PWD, NAGALAND	03/2019	237.51 -	12/2022 -	12/2022	0/0
948	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD, CHHATISGARH	12/2015	291.05 -	- -	-	0/0
949	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD, CHHATISGARH	11/2015	485.44 -	12/2015 -	-	0/0
950	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD, ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-	0/0
951	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD, ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-	0/0
952	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD, ARUNACHAL PRADESH	03/2012	207.03 389.45	05/2012 06/2018	-	0/0
953	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD, SIKKIM	04/2013	166.27 203.26	08/2013 -	-	0/0
954	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD, NAGALAND	12/2010	1,296.00 -	02/2011 -	-	0/0
955	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]PWD, UTTAR PRADESH	11/2010	305.49 -	03/2017 -	-	0/0
956	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD, MADHYA PRADESH	01/2012	320.48 -	08/2015 -	-	0/0
957	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD, PUNJAB	12/2015	766.36 -	- 09/2019	-	0/0
958	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD, PUNJAB	11/2015	847.02 -	- 09/2019	-	0/0
959	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD, PUNJAB	11/2015	889.24 -	- 12/2019	-	0/0
960	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD, ASSAM	11/2010	268.08 -	05/2017 -	-	0/0
961	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD, ASSAM	11/2010	470.20 -	02/2011 -	-	0/0
962	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD, ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-	0/0
963	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD, ASSAM	11/2014	218.31 307.47	02/2018 -	-	0/0
964	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD, ODISHA	07/2014	342.05 -	01/2017 -	-	0/0
965	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD, RAJASTHAN	09/2012	511.00 -	10/2013 -	-	0/0
966	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD, PUNJAB	06/2015	892.17 -	- -	-	0/0
967	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD, BIHAR	01/1991	154.62 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
968	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-	0/0
969	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA	03/2016	1,142.62 -	- -	-	0/0
970	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA	03/2016	1,101.58 -	- -	-	0/0
971	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]PWD,WEST BENGAL	01/2017	396.86 396.86	09/2019 -	-	0/0
972	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]PWD,UTTAR PRADESH	11/2016	326.99 327.00	- -	-	0/0
973	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) - [N24000908]PWD,HARYANA	01/2017	276.01 -	03/2019 07/2019	-	0/0
974	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]PWD,GUJARAT	10/2018	400.76 -	05/2019 -	-	0/0
975	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037 OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]PWD,TELANGANA	01/2017	244.54 -	05/2019 09/2019	-	0/0
976	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]PWD,TELANGANA	01/2019	193.19 -	- -	-	0/0
977	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]PWD,BIHAR	03/2018	153.24 -	- -	-	0/0
978	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT - [N24001154]PWD,KARNATAKA	08/2016	367.44 -	01/2017 -	-	0/0
979	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT - [N24001155]PWD,KARNATAKA	08/2016	175.20 -	01/2017 -	-	0/0
980	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS - PA - [N24001156]PWD,KARNATAKA	01/2017	166.67 -	09/2017 -	-	0/0
981	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]PWD,KARNATAKA	08/2016	175.50 -	02/2017 -	-	0/0
982	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]PWD,KARNATAKA	03/2018	159.97 -	06/2019 -	-	0/0
983	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]PWD,KARNATAKA	01/2018	159.70 -	07/2018 -	-	0/0
984	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]PWD,KARNATAKA	09/2017	191.60 -	10/2018 -	-	0/0
985	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]PWD,KARNATAKA	12/2017	297.30 -	01/2019 -	-	0/0
986	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]PWD,KARNATAKA	03/2018	325.86 -	10/2018 -	-	0/0
987	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]PWD,KARNATAKA	08/2016	329.01 -	02/2017 -	-	0/0
988	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]PWD,KARNATAKA	10/2016	396.96 -	03/2017 -	-	0/0
989	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]PWD,KARNATAKA	11/2016	314.90 -	03/2017 -	-	0/0
990	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]PWD,KARNATAKA	03/2015	159.12 -	01/2016 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
991	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776) - [N24001167]PWD,KARNATAKA	03/2015	165.67 -	01/2016 -	-	0/0
992	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM. - [N24001170]PWD,KARNATAKA	01/2014	471.16 -	08/2014 -	-	0/0
993	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]PWD,KARNATAKA	01/2017	291.49 -	08/2017 -	-	0/0
994	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S - [N24001183]PWD,ANDHRA PRADESH	07/2014	251.55 -	02/2015 -	-	0/0
995	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]PWD,ARUNACHAL PRADESH	11/2016	243.89 -	- -	-	0/0
996	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]PWD,BIHAR	02/2019	2,926.42 -	- -	-	0/0
997	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]PWD,UTTAR PRADESH	03/2018	306.59 -	- -	-	0/0
998	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]PWD,UTTAR PRADESH	11/2018	281.45 -	- -	-	0/0
	<u>SHIPPING AND PORTS</u>					
	<u>Inland Waterways Authority Of India</u>					
999	JAL MARG VIKAS PROJECT - [N25000072]IWAI,MULTI STATE	01/2018	4,200.00 5,369.18	03/2023 03/2023	03/2023	0/0
	<u>TELECOMMUNICATIONS</u>					
	<u>Bharat Sanchar Nigam Limited</u>					
1000	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]BSNL,MAHARASHTRA	01/2018	231.80 240.10	10/2018 12/2019	12/2019	0/0
	<u>Department Of Telecommunication</u>					
1001	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	07/2015 -	05/2020	0/0
	<u>Mahanagar Telephone Nigam Limited</u>					
1002	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI	06/2016	418.26 -	06/2017 -	-	0/0
	<u>URBAN DEVELOPMENT</u>					
	<u>Ahmedabad Metro Rail</u>					
1003	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT	11/2014	10,773.00 -	12/2018 -	07/2020	0/0
	<u>Bangalore Metro Rail Corporation Limited</u>					
1004	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	02/2019 -	03/2020	0/0
	<u>Central Public Works Department</u>					
1005	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	12/2013 -	10/2019	0/0
1006	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI	10/2017	271.90 -	11/2019 -	11/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
1007	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN	12/2016	549.31 559.47	07/2019 12/2019	02/2020	0/0
1008	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH	11/2017	171.72 -	03/2020 -	03/2020	0/0
1009	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD,DELHI	11/2017	238.56 -	05/2020 -	05/2020	0/0
1010	RESIDENTIAL QUATERS FOR HAL,BANGLORE - [N28000103]CPWD,KARNATAKA	12/2016	246.31 -	02/2020 -	09/2020	0/0
1011	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	06/2017 -	10/2020	0/0
1012	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00 -	- -	12/2020	0/0
1013	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 -	- 08/2020	03/2021	0/0
1014	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU	11/2017	348.77 -	- -	11/2021	0/0
1015	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD,ODISHA	01/2019	790.79 -	03/2022 -	03/2022	0/0
1016	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	12/2015 -	-	0/0
1017	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]CPWD,DELHI	12/2017	188.00 -	06/2019 -	-	0/0
1018	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI	10/2016	248.20 -	04/2018 -	-	0/0
1019	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI - [N28000123]CPWD,DELHI	07/2017	218.72 -	- -	-	0/0
	<u>Hindustan Steelwork Construction Limited</u>					
1020	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	03/2015 -	03/2021	0/0
1021	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	12/2015 -	-	0/0
1022	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	12/2016 -	-	0/0
1023	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	12/2016 -	-	0/0
1024	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,070.97	02/2014 -	-	0/0
1025	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 324.87	12/2015 -	-	0/0
1026	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	09/2017 -	-	0/0
1027	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	- -	-	0/0
1028	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL,GUJARAT	01/2013	175.00 -	- -	-	0/0
1029	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	03/2017 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
1030	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 253.92	06/2016 -	-	0/0
1031	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND	12/2007	200.00 -	03/2018 -	-	0/0
1032	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	12/2016 -	-	0/0
1033	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND	04/2013	170.00 -	04/2018 -	-	0/0
1034	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL	08/2012	185.37 -	03/2016 -	-	0/0
	<u>Jawahar Lal Nehru National Urban Renewal Mission</u>					
1035	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-	0/0
	<u>Kochi Metro Rail Corporation Ltd</u>					
1036	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	07/2017 -	12/2019	0/0
	<u>Lucknow Metro Rail Corporation Limited</u>					
1037	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	-	0/0
	<u>Maharastra Metro Rail Corporation Ltd.</u>					
1038	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA	12/2016	11,420.00 -	11/2021 01/2022	01/2022	0/0
1039	DELHI MRTS PHASE-III - [N28000056]MMRC,DELHI	09/2011	38,585.00 -	03/2016 -	-	0/0
	<u>Mumbai Metro Rail Corporation Ltd</u>					
1040	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	05/2020	0/0
	<u>Madhya Pradesh Metro Rail Co Limited</u>					
1041	BHOPAL METRO RAIL - [N28000124]MPMRCL,MADHYA PRADESH	11/2018	6,941.40 -	02/2023 -	02/2023	0/0
1042	INDORE METRO RAIL - [N28000125]MPMRCL,MADHYA PRADESH	11/2018	7,500.80 -	02/2023 -	02/2023	0/0
	<u>Nagpur Metro Rail Corporation Ltd</u>					
1043	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	12/2019	0/0
	<u>National Building Construcion Corporation Ltd</u>					
1044	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI	07/2016	2,694.00 -	- -	-	0/0
	<u>WATER RESOURCES</u>					
	<u>Brahmaputra Board</u>					
1045	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPB,MAHARASHTRA	03/2017	233.57 -	12/2019 -	12/2019	0/0
	Total		11,40,968.45 -			0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (September 2019)						
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	Grand Total		11,40,968.45			0/0

List of Projects Ahead of Schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
	<u>South-Eastern Coal Fields Limited</u>						
1	BATURA OCP (2.0 MTY) - [N06000049]	8/2015	1,186.64 -	203.82	121.39	03/2023 -	03/2021
	Total		1,186.64 -	203.82	121.39		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
2	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]	2/2016	554.00 -	554.00	363.86	02/2020 -	10/2019
	<u>Indian Oil Corporation Limited</u>						
3	PARADIP HYDERABAD PIPELINE - [N16000194]	1/2015	2,321.00 3,338.00	3,338.00	1,820.56	12/2020 -	08/2020
4	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]	9/2015	324.00 -	324.00	154.50	06/2020 -	03/2020
5	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL [N16000252]	5/2016	664.00 -	664.00	601.75	12/2020 -	02/2020
6	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]	8/2017	315.00 -	315.00	112.13	12/2021 -	12/2020
7	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]	3/2018	3,712.00 -	3,696.00	309.62	09/2022 -	06/2021
8	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]	8/2017	384.58 -	384.58	85.86	04/2021 -	04/2020
	Total		8,274.58 -	9,275.58	3,448.28		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
9	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	1/2013	12,964.60 17,304.00	17,304.00	13,970.00	05/2018 12/2021	03/2021
	Total		12,964.60 -	17,304.00	13,970.00		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
10	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	2/2015	3,627.47 -	3,627.47	686.42	03/2024 -	03/2022
	<u>East Central Railways</u>						

Costing Rs. 150 Crore and above

(September 2019)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
11	GARHWA ROAD-RAMNA - [N22000465]	3/2015	348.23 -	348.23	177.12	03/2021 -	12/2020
	<u>North East Frontier Railway</u>						
12	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	4/2015	2,232.32 -	2,182.00	654.38	03/2022 -	03/2020
13	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) [N22000390]	4/2016	602.27 -	612.00	257.73	12/2021 -	03/2020
	<u>North Eastern Railway</u>						
14	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,295.42 -	1,295.42	328.56	03/2022 -	12/2019
	<u>Rail Vikas Nigam Ltd.</u>						
15	BHANUPALI-BILASPUR BERI NL - [N22000273]	4/2008	2,966.99 -	7,000.00	398.76	12/2026 -	12/2025
16	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78 -	723.78	0.19	12/2025 -	03/2025
	Total		11,796.48 -	15,788.90	2,503.16		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways</u>						
17	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]	2/2017	429.43 -	429.43	203.52	11/2017 03/2020	11/2019
18	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969]	1/2017	263.45 -	263.45	57.97	09/2017 03/2020	09/2019
19	PARSHURAM GHAT TO ARAWALI - [N24001133]	4/2016	983.14 983.14	983.14	655.15	12/2019 -	11/2019
20	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]	1/2017	576.48 -	576.48	207.93	01/2018 03/2020	01/2020
	<u>National Highways Authority Of India</u>						
21	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]	10/2015	447.29 746.43	746.43	600.33	12/2017 06/2020	12/2019
22	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199 (DESIGN CHAINAGE) - [N24000600]	8/2016	1,388.34 2,525.80	2,525.80	1,449.00	09/2019 03/2020	09/2019
23	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]	3/2017	247.02	157.49	21.89	03/2020 02/2021	02/2020
24	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]	3/2017	296.19 -	254.00	248.60	03/2020 -	09/2019
25	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]	3/2017	639.79	552.90	491.93	03/2020 -	09/2019
26	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]	3/2017	648.32 -	503.10	497.15	03/2020 -	11/2019

Costing Rs. 150 Crore and above

(September 2019)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
27	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669	3/2017	165.50	172.16	117.09	03/2020 -	09/2019
28	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691	4/2017	894.00 -	894.00	730.00	04/2020 -	11/2019
	<u>Public Works Dept Of State</u>						
29	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904	1/2017	247.25 -	247.25	144.71	03/2019 03/2020	09/2019
	Total		7,226.20 -	8,305.63	5,425.27		
	Grand Total		41,448.50	50,877.93	25,468.10		

List of Projects on schedule w.r.t. Latest Schedule

Annexure - XII

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
1	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]	8/2018	951.28 -	951.28	71.55	10/2021 -	10/2021
2	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]	6/2018	1,383.00 -	1,383.00	210.62	09/2021 -	09/2021
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT - [N04000079]	3/2017	358.89 -	358.89	29.73	04/2021 -	04/2021
4	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA - [N04000081]	1/2019	264.99 -	264.99	.42	11/2021 -	11/2021
5	CONSTRUCTION OF TERMINAL BUILDING & ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	7/2018	323.19 -	323.19	10.14	09/2021 -	09/2021
6	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082]	5/2018	539.20 -	539.20	25.64	10/2022 -	10/2022
7	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN - [N04000085]	7/2018	353.27 -	353.27	114.29	09/2020 -	09/2020
8	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]	12/2016	859.86 -	860.00	232.44	03/2021 -	03/2021
	Total		5,033.68 -	5,033.82	694.83		
	<u>COAL</u>						
	<u>Bharat Coking Coal Limited</u>						
9	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	5.24	03/2021 -	03/2021
	<u>Central Coal Fields Limited</u>						
10	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	194.12	03/2020 -	03/2020
11	NORTH URIMARI EXPANSION OCP - [N06000182]	3/2019	1,553.06 -	1,553.06	163.23	03/2023 -	03/2023
	<u>Eastern Coal Fields Limited</u>						
12	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	315.69	03/2022 -	03/2022
13	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	83.23	03/2022 -	03/2022
14	SIDULI MINE (OC AND UG) - [N06000165]	5/2018	535.18 -	535.18	-	03/2026 -	03/2026

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
15	NAKRAKONDA KUMARDIH B OCP - [N06000170]	8/2018	502.68 -	502.68	-	03/2029 -	03/2029
16	TILABONI UG MINE - [N06000172]	2/2019	916.62 -	916.62	-	03/2027 -	03/2027
17	CHITRA EAST (RCE) OCP - [N06000169]	8/2018	513.98 -	513.98	90.23	03/2024 -	03/2024
	<u>Mahanadi Coal Fields Limited</u>						
18	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	1,549.76	03/2026 -	03/2026
19	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]	5/2018	2,434.75 -	2,434.75	83.20	03/2027 -	03/2027
20	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]	11/2018	2,838.87 -	2,838.87	1,113.66	03/2029 -	03/2029
21	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	440.13	03/2021 -	03/2021
	<u>Neyveli Lignite Corporation</u>						
22	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	7,532.67	11/2021 -	11/2021
	<u>Northern Coal Fields Limited</u>						
23	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]	5/2017	1,783.09 -	1,783.09	267.80	03/2021 -	03/2021
24	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]	11/2017	1,255.17 -	1,255.17	95.24	03/2022 -	03/2022
25	BLOCK-B EXPANSION OPENCAST PROJECT - [N06000184]	7/2019	998.71 -	998.71	-	03/2023 -	03/2023
26	SEMARIA OPENCAST PROJECT - [N06000176]	5/2019	396.58 -	396.58	-	03/2026 -	03/2026
	<u>Singareni Colliers Company Limited</u>						
27	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]	12/2015	477.65 -	477.65	2.11	03/2020 -	03/2020
	<u>South-Eastern Coal Fields Limited</u>						
28	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	6.42	03/2023 -	03/2023
29	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	102.91	03/2022 -	03/2022
30	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
31	MALACHUA OPENCAST PROJECT - [N06000139]	10/2015	488.33 -	488.33	27.10	03/2023 -	03/2023
32	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	82.91	03/2020 -	03/2020
33	JHIRIA WEST OPENCAST PROJECT - [N06000166]	11/2018	389.97 -	389.97	-	03/2026 -	03/2026
34	MAHAMAYA OPENCAST PROJECT - [N06000164]	5/2018	410.26 -	410.26	9.53	03/2026 -	03/2026
35	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	75.96	03/2026 -	03/2026

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
36	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]	3/2016	869.44 -	869.44	116.48	03/2021 -	03/2021
37	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]	6/2010	11,816.40 -	11,816.40	2,882.36	03/2023 -	03/2023
38	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	2,057.57	03/2023 -	03/2023
39	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	4.02	03/2023 -	03/2023
40	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	73.31	03/2020 -	03/2020
41	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
42	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	52.43	03/2021 -	03/2021
43	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	104.06	03/2021 -	03/2021
44	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
	<u>Western Coal Fields Limited</u>						
45	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	182.76	03/2020 -	03/2020
46	GANDHIGRAM UG MINE - [N06000183]	8/2019	414.16 -	414.16	-	03/2026 -	03/2026
47	BELLORA-NAIGAON DEEP OC - [N06000180]	11/2018	252.71 -	252.71	44.94	03/2021 -	03/2021
48	UKNI DEEP OC - [N06000179]	11/2018	318.14 -	318.14	146.45	03/2021 -	03/2021
49	VISHNUPURI UG TO OC MINE - [N06000178]	7/2018	195.57 -	195.57	2.94	03/2025 -	03/2025
50	SAONER I UG TO OC PHASE I - [N06000177]	11/2016	162.10 -	162.10	50.56	03/2022 -	03/2022
51	KOLAR PIMPRI EXTENSION OC - [N06000160]	3/2017	362.73 -	362.73	319.93	03/2020 -	03/2020
52	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]	2/2017	328.00 -	328.00	160.15	03/2021 -	03/2021
53	DHANKASA UG (1.00 MTY) - [N06000155]	9/2016	458.07 -	458.07	20.86	03/2022 -	03/2022
54	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	319.76	235.33	03/2022 -	03/2022
55	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]	7/2016	409.87 -	409.87	20.30	03/2022 -	03/2022
56	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	210.32	03/2021 -	03/2021
57	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	268.58	03/2025 -	03/2025
58	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	121.74	03/2020 -	03/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
59	PENGANGA OCP(REVISED) - [N06000066	9/2014	441.82 -	441.82	213.24	03/2020 -	03/2020
60	DINESH OCP - [N06000118	11/2014	611.16 -	611.16	413.13	03/2020 -	03/2020
61	BHANEAGAON OC - [N06000121	2/2015	187.94 -	409.68	128.90	03/2023 -	03/2023
	Total		74,841.58 -	75,064.12	20,071.50		
	<u>FERTILISERS</u>						
	<u>National Fertiliser Limited</u>						
62	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014	1/2018	215.92 -	215.92	117.03	11/2019 -	11/2019
63	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015	1/2018	218.83 -	218.83	119.23	11/2019 -	11/2019
64	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016	1/2018	239.81 -	239.81	134.46	11/2019 -	11/2019
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
65	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018	4/2018	426.72 -	426.72	197.47	04/2020 -	04/2020
	Total		1,101.28 -	1,101.28	568.19		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>National Building Construcion Corporation Ltd</u>						
66	AIIMS BILASPUR - [N21000028	4/2018	1,351.00 -	1,351.00	137.87	09/2021 -	09/2021
	Total		1,351.00 -	1,351.00	137.87		
	<u>HEAVY INDUSTRY</u>						
	<u>Bharat Heavy Electricals Limited</u>						
67	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002	8/2016	1,554.00 -	1,554.00	335.03	09/2019 -	09/2019
	Total		1,554.00 -	1,554.00	335.03		
	<u>INFORMATION AND BROADCASTING</u>						
	<u>National Building Construcion Corporation Ltd</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
68	NATIONAL CENTRE OF EXCELLENCE FOR ANIMATION VISUAL EFFECTS GAMING AND COMICS [N09000003]	12/2016	167.70 -	167.70	-	03/2020 -	03/2020
	Total		167.70 -	167.70	.00		
	<u>MINES</u>						
	<u>National Aluminum Company Limited (Nalco)</u>						
69	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	5,540.00 -	5,540.00	107.45	04/2021 04/2021	04/2021
70	UTKAL D AND E COAL BLOCK - [N10000011]	5/2016	534.00 -	534.00	319.23	01/2020 -	01/2020
71	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]	11/2017	483.00 -	483.00	.30	04/2021 04/2021	04/2021
72	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]	12/2015	355.00 -	355.00	31.92	11/2020 -	11/2020
	Total		6,912.00 -	6,912.00	458.90		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
73	HALDIA LPG IMPORT FACILITY - [N16000223]	3/2015	694.00 -	1,097.54	700.96	10/2018 12/2019	12/2019
74	MMPL PIPELINE REROUTING PROJECT - [N16000261]	4/2013	449.58 -	449.58	155.32	12/2019 -	12/2019
75	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY [N16000263]	2/2016	3,313.00 -	3,288.96	1,151.10	02/2020 10/2020	10/2020
76	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29 -	5,245.96	3,711.38	08/2018 11/2019	11/2019
77	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]	12/2015	1,112.00 -	1,507.24	525.00	06/2019 02/2022	02/2022
78	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]	9/2018	11,130.00 -	11,130.00	18.14	03/2023 -	03/2023
79	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. [N16000373]	11/2018	248.55 -	248.55	22.86	06/2022 -	06/2022
80	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL [N16000365]	12/2017	1,524.06 -	1,524.06	13.73	12/2021 -	12/2021
81	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT [N16000364]	7/2017	580.20 -	580.20	38.21	02/2021 -	02/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
82	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]	10/2018	206.26 -	206.26	.98	03/2021 -	03/2021
83	2G ETHANOL BIO REFINERY AT BARGARH - [N16000341]	8/2017	750.00 -	750.00	34.73	12/2020 -	12/2020
84	PUNE POL STORAGE DEPOT - [N16000313]	8/2016	282.64 -	282.64	127.11	08/2020 -	08/2020
	<u>Chennai Petroleum Corporation Limited</u>						
85	BS-VI PROJECTS - [N16000295]	9/2017	1,858.00 -	1,858.00	1,026.86	12/2019 -	12/2019
86	RE-LIQUIFIED NATURAL GAS - [N16000301]	8/2017	421.00 -	421.00	137.46	08/2020 -	08/2020
	<u>Gas Authority Of India Limited</u>						
87	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	2/2015	749.00 -	842.00	606.89	02/2020 -	02/2020
88	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]	3/2017	2,433.00 -	2,433.00	1,441.96	12/2020 -	12/2020
89	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	3/2017	1,740.00 -	1,740.00	275.95	12/2020 -	12/2020
90	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	287.49	125.82	04/2022 -	04/2022
91	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]	8/2018	286.42 -	286.42	1.93	08/2020 09/2020	09/2020
92	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]	9/2018	225.54 -	225.54	1.41	02/2021 -	02/2021
93	BARAUNI-GUWAHATI PIPELINE - [N16000334]	6/2018	3,308.00 -	3,308.00	1,250.10	12/2021 -	12/2021
94	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR - [N16000330]	10/2017	221.45 -	221.45	46.15	10/2022 -	10/2022
95	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329]	10/2017	226.45 -	226.45	50.15	10/2022 -	10/2022
96	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]	7/2017	182.20 -	182.20	30.42	07/2022 -	07/2022
97	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]	10/2017	359.25 -	359.25	68.16	10/2022 -	10/2022
98	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]	7/2017	243.53 -	243.53	52.38	07/2022 -	07/2022
99	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]	3/2017	3,437.00 -	3,437.00	1,271.51	12/2020 -	12/2020
100	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	3/2017	1,933.00 -	1,933.00	1,035.77	12/2020 -	12/2020
101	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]	7/2015	2,881.40 -	2,000.00	1,285.47	12/2020 -	12/2020
	<u>Hindustan Petroleum Corporation Limited</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
102	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,928.00 -	20,928.00	6,455.02	07/2020 -	07/2020
103	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA [N16000312]	11/2017	255.00 -	255.00	75.50	11/2020 -	11/2020
104	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]	9/2015	4,199.00 -	5,060.00	2,754.00	03/2020 -	03/2020
105	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367]	6/2019	2,166.38 -	2,166.38	9.80	06/2022 -	06/2022
106	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE [N16000369]	12/2018	854.00 -	854.00	38.34	12/2022 -	12/2022
107	REDEVELOPMENT/ EXPANSION OF MEERUT DEPOT FOR ENHANCING PRODUCT HANDLING CAPACITY - [N16000366]	8/2016	154.84 -	154.84	120.67	11/2019 -	11/2019
108	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]	9/2016	1,879.00 -	1,879.00	1,476.87	06/2020 -	06/2020
109	EXTENSION OF VISAKH-VIJAYAWADA- SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	9/2017	2,677.00 -	2,677.00	894.02	03/2021 -	03/2021
	<u>Indian Oil Corporation Limited</u>						
110	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]	5/2013	711.00 -	711.00	11.12	06/2020 -	06/2020
111	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]	2/2015	890.00 -	887.00	603.29	10/2019 -	10/2019
112	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY [N16000321]	4/2018	206.63 -	206.63	13.75	02/2020 -	02/2020
113	LPG BP PROJECT MOTIHARI - [N16000317]	5/2018	206.50 -	206.50	13.88	03/2021 -	03/2021
114	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309]	8/2017	1,342.00 -	1,342.00	6.30	08/2020 -	08/2020
115	AUGMENTATION OF CTMPL - [N16000286]	12/2016	228.00 -	228.00	15.40	06/2020 -	06/2020
116	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]	9/2016	208.35 -	208.35	123.99	07/2020 -	07/2020
117	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]	5/2016	261.00 -	261.00	41.42	01/2021 -	01/2021
118	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM [N16000270]	7/2014	247.00 -	247.00	-	03/2021 -	03/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
119	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]	1/2015	342.00 -	342.00	-	03/2021 -	03/2021
120	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]	4/2016	1,021.00 -	1,021.00	4.45	12/2020 -	12/2020
121	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]	10/2018	1,297.50 -	1,297.50	10.17	10/2021 -	10/2021
122	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]	4/2018	522.00 -	522.00	142.71	03/2021 -	03/2021
123	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]	8/2018	1,636.00 -	1,636.00	148.87	08/2020 -	08/2020
124	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]	8/2018	557.00 -	557.00	217.83	02/2020 -	02/2020
125	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]	4/2018	5,654.00 -	5,654.00	344.69	10/2021 -	10/2021
126	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]	7/2018	189.00 -	189.00	9.15	01/2021 -	01/2021
127	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]	3/2018	676.00 -	676.00	168.18	12/2021 -	12/2021
128	DEVELOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]	12/2017	199.36 -	199.36	9.39	10/2020 -	10/2020
129	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]	8/2017	255.40 -	255.40	1.75	08/2020 -	08/2020
130	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT - [N16000363]	12/2018	278.60 -	278.60	-	06/2021 -	06/2021
131	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]	5/2019	3,361.00 -	3,361.00	325.72	08/2021 -	08/2021
132	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]	11/2018	462.30 -	462.30	-	09/2021 -	09/2021
133	120 TMTPL LPG BOTTLING PLANT AT GORAKHPUR UP - [N16000354]	3/2014	204.00 -	204.00	139.25	09/2019 -	09/2019
134	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]	10/2018	598.00 -	598.00	15.22	02/2020 -	02/2020
135	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]	1/2019	909.00 -	909.00	16.17	01/2021 -	01/2021
136	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]	12/2018	611.00 -	611.00	1.68	04/2022 -	04/2022
137	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]	10/2018	316.20 -	316.20	14.78	10/2021 -	10/2021
138	FUEL QUALITY UPGRADATION (NSU,NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY - [N16000348]	6/2017	951.64 -	951.64	399.12	10/2019 -	10/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
139	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]	6/2019	371.00 -	371.00	-	09/2022 -	09/2022
140	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	960.09	08/2021 -	08/2021
141	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]	2/2016	2,582.00 -	2,582.00	1,557.14	11/2019 -	11/2019
142	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	1/2015	1,823.00 -	3,027.90	861.98	12/2020 -	12/2020
<u>Mangalore Refinery And Petrochemicals Limited</u>							
143	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]	10/2015	135.00 171.00	170.70	156.65	03/2019 10/2019	10/2019
144	BSVI UPGRADEATION - [N16000257]	9/2016	1,810.00 1,810.00	1,810.00	823.40	12/2019 07/2020	07/2020
<u>Oil & Natural Gas Corporation Limited</u>							
145	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]	3/2009	2,465.15 -	2,378.86	2,147.00	03/2013 12/2019	12/2019
146	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]	8/2015	2,818.88 -	2,818.88	2,230.96	03/2019 05/2020	05/2020
147	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	1,908.01	03/2015 12/2019	12/2019
148	GAS COMPRESSOR PROJECT AT ANKLESHWAR ASSET (GCP-ANK) - [N16000371]	10/2018	156.67 -	156.67	-	03/2021 -	03/2021
149	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]	5/2019	763.92 -	763.92	-	12/2020 -	12/2020
150	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) - [N16000335]	4/2018	766.37 -	766.37	449.88	12/2019 -	12/2019
151	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]	2/2017	4,006.83 -	4,475.92	2,796.50	05/2021 12/2021	12/2021
152	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]	2/2017	968.61 -	1,033.95	930.62	11/2019 -	11/2019
153	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]	2/2017	511.30 -	511.30	476.47	11/2019 -	11/2019
154	DEVELOPMENT OF B-147 FIELD - [N16000292]	2/2017	546.15 -	565.15	442.18	11/2019 03/2020	03/2020
155	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]	4/2017	420.76 -	407.45	239.45	09/2018 09/2019	09/2019
156	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	1,162.56	392.39	03/2026 -	03/2026
157	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	7/2016	249.85 250.00	265.49	157.81	05/2020 -	05/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
158	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	2,225.67	04/2018 05/2020	05/2020
159	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]	11/2015	650.82 -	650.82	394.21	03/2019 05/2020	05/2020
160	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]	4/2019	3,228.80 -	3,228.80	458.52	03/2022 -	03/2022
161	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]	2/2019	2,292.46 -	2,292.46	300.13	05/2021 -	05/2021
162	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	823.27 -	910.23	356.00	03/2023 03/2022	03/2022
163	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]	1/2015	4,619.94 -	4,619.94	4,360.59	12/2017 03/2020	03/2020
164	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	3/2011	861.79 -	1,683.06	1,322.31	05/2013 12/2019	12/2019
165	DAMAN DEVELOPMENT PROJECT - [N16000198]	8/2014	6,086.08 -	5,842.31	4,784.88	05/2019 10/2019	10/2019
166	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]	11/2014	6,068.80 -	5,296.93	4,758.62	04/2019 12/2019	12/2019
	<u>Oil India Limited</u>						
167	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]	5/2016	406.00 -	406.00	88.85	10/2020 -	10/2020
168	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN - [N16000356]	6/2016	224.75 -	224.75	4.37	08/2020 -	08/2020
169	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]	9/2016	571.66 -	571.66	200.97	12/2019 -	12/2019
	Total		1,57,713.75 -	1,61,480.94	65,616.06		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
170	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	12,865.92	12,188.01	01/2018 03/2020	03/2020
171	PATRATU STPP-I (3X800MW) - [N18000275]	11/2017	18,668.00 -	18,668.00	2,004.32	03/2023 -	03/2023
172	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000274]	3/2019	349.00 -	349.00	125.00	11/2020 -	11/2020
173	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000273]	12/2018	587.44 -	587.44	250.00	09/2020 -	09/2020
174	TALAIPALLI COAL MINING PROJECT - [N18000266]	9/2015	3,004.00 -	3,004.00	1,610.00	11/2019 -	11/2019
175	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	1/2016	10,598.98 -	10,598.98	5,557.96	11/2020 06/2021	06/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
176	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	11,148.86	8,619.60	01/2020 -	01/2020
177	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	12,457.15	10/2017 03/2020	03/2020
178	BARH STPP(3X660MW) NTPC - [180100242]	2/2005	8,692.97 -	21,312.11	16,453.44	10/2011 08/2021	08/2021
179	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]	4/2012	9,750.89 -	12,176.28	9,794.00	02/2017 06/2020	06/2020
180	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,592.34	486.24	09/2019 02/2022	02/2022
	<u>North East Electric Power Corporation</u>						
181	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	7,927.34	7,579.17	12/2009 10/2019	10/2019
	<u>Power Grid Corporation Of India Limited</u>						
182	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]	5/2016	14,733.37 -	14,733.37	8,796.37	11/2019 -	11/2019
183	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII [N18000245]	3/2017	379.95 -	379.95	76.66	12/2019 -	12/2019
184	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]	2/2017	5,070.13 -	5,070.13	2,771.21	04/2020 -	04/2020
185	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	3/2017	3,500.00 3,500.00	3,500.00	1,758.00	07/2020 -	07/2020
186	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]	11/2017	358.83 -	358.83	121.83	05/2020 -	05/2020
187	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]	8/2017	1,931.39 -	1,931.39	1,054.28	02/2020 -	02/2020
188	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]	2/2017	195.05 -	195.05	120.83	02/2020 -	02/2020
189	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]	3/2017	283.72 -	283.72	193.70	11/2019 -	11/2019
	<u>Satluj Jal Vidyut Nigam Limited</u>						
190	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]	3/2019	10,439.09 -	10,439.09	780.04	01/2024 -	01/2024
191	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	648.33	265.90	12/2021 -	12/2021
	<u>Thdc India Limited</u>						
192	AMELIA COAL MINE - [N18000252]	1/2017	2,104.21 -	1,587.16	307.48	09/2020 -	09/2020
193	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]	3/2019	11,089.42 -	11,089.42	521.82	09/2023 -	09/2023
	Total		1,39,618.57 -	1,63,186.53	93,893.01		

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
194	WARDHA-NANDED MAHARASHTRA - [N22000231	4/2008	3,168.29 -	3,168.29	1,202.43	03/2023 -	03/2023
195	PUNE-NASIK (265 KM) - [N22000354	2/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024
196	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355	2/2016	2,750.00 -	3,438.51	-	03/2024 -	03/2024
197	DAUND - MANMAD (236 KM) - [N22000360	2/2016	1,876.00 -	2,081.27	121.17	03/2023 -	03/2023
198	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358	2/2015	2,449.91 -	2,449.91	165.28	03/2023 -	03/2023
199	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247	4/2011	184.06 -	305.00	269.39	03/2019 12/2019	12/2019
200	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353	2/2016	9,968.00 -	9,968.00	-	03/2024 -	03/2024
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
201	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	03/2020
	<u>East Central Railways</u>						
202	KOSI BRIDGE (NL), ECR - [220100304	4/2002	499.41 -	516.02	397.11	03/2020 -	03/2020
203	ARARIA-SUPAUL (NL) - [N22000177	4/2008	1,605.17 -	1,605.17	23.49	- 03/2023	03/2023
	<u>East Coast Railway</u>						
204	BHADRAK - NERGUNDI 3RD LINE - [N22000316	3/2013	843.04 -	843.04	133.25	10/2020 03/2023	03/2023
205	KOTTAVALSA - KORAPUT DOUBLING - [N22000377	4/2015	2,499.71 -	3,382.95	373.22	03/2022 -	03/2022
206	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381	4/2015	1,172.92 -	1,172.92	397.91	12/2018 03/2022	03/2022
	<u>Metropolitan Rapid Transport Projects</u>						
207	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	4/2008	5,300.00 -	918.53	284.75	03/2014 03/2021	03/2021
	<u>North Central Railway</u>						
208	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372	4/2015	668.70 668.00	680.00	330.00	03/2020 -	03/2020
209	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495	3/2018	4,329.53 -	4,329.53	3.90	03/2023 -	03/2023
210	JHANSI BINA DOUBLING - [N22000496	9/2016	2,001.00 -	2,001.00	416.59	03/2021 -	03/2021
	<u>North East Frontier Railway</u>						
211	BHAIRABI SAIRONG, NL, NEFR - [N22000100	4/2008	2,393.47 -	5,021.45	3,075.08	03/2014 03/2022	03/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
212	DIGARU-HOJAI (102 KM) - [N22000389]	4/2015	870.96 -	2,136.01	502.44	03/2021 -	03/2021
213	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	4/2010	906.46 -	6,000.00	261.76	03/2021 -	03/2021
214	MURKONGSELEK-PASIGHAT NL - [N22000208]	4/2011	414.84 -	661.00	122.05	03/2020 -	03/2020
215	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	4/2010	242.22 -	471.00	68.15	03/2020 -	03/2020
216	DIMAPUR-TIZIT NL - [N22000196]	4/2013	4,274.00 -	4,274.00	-	03/2020 -	03/2020
217	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	4/2008	333.76 -	360.00	6.67	- 03/2022	03/2022
218	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	4/2010	221.42 -	380.00	38.18	- 03/2022	03/2022
	<u>North Eastern Railway</u>						
219	HATHUA-BHATNI (N L) (NER) - [220100319]	4/2005	230.03 -	230.03	277.14	12/2022 -	12/2022
220	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	3/2007	243.78 -	895.00	106.55	12/2021 -	12/2021
221	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]	4/2016	600.00 -	600.00	25.24	01/2022 -	01/2022
222	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]	4/2016	1,900.00 -	1,277.06	-	01/2022 -	01/2022
	<u>Northern Railway</u>						
223	CHANDIGARH-BADDI - [N22000467]	4/2007	328.14 -	1,540.00	233.84	03/2023 -	03/2023
	<u>National High Speed Rail Corporation Limited</u>						
224	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]	12/2015	1,08,000.00 -	1,08,000.00	4,886.79	12/2023 12/2023	12/2023
	<u>Rail India Technical And Economic Service</u>						
225	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	281.85	03/2021 -	03/2021
226	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498]	2/2016	393.98 -	393.98	241.23	03/2020 -	03/2020
	<u>Rail Vikas Nigam Ltd.</u>						
227	AHMEDABAD-BOTAD (GC) - [N22000140]	4/2012	975.62 -	1,082.32	994.30	12/2021 -	12/2021
228	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	773.94 -	773.94	413.71	12/2024 -	12/2024
229	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE- GUNTAKAL -ELECTRIFICATION (641.37 KM) [N22000407]	3/2009	713.48 -	1,950.00	1,957.22	03/2020 -	03/2020
230	DHASA-JETALSAR (GC) - [N22000141]	4/2012	644.38 -	644.38	352.02	03/2021 -	03/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
231	VIJAYAWADA-GUDUR - [N22000369	4/2015	3,246.26 -	3,548.67	1,072.89	12/2023 -	12/2023
232	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409	1/1991	2,335.67 -	2,335.68	598.12	12/2024 -	12/2024
	<u>South Central Railway</u>						
233	BHADRACHALAM ROAD-SATTUPALLI - [N22000287	4/2010	704.31 -	1,352.74	269.07	03/2020 -	03/2020
234	MANMAD-PARBHANI-NANDED-SECUNDERABAD- GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432	4/2017	119.73 185.00	184.97	3.67	03/2022 -	03/2022
	<u>South East Central Railway</u>						
235	GONDIA-JABALPUR(GC),(SECR) - [220100186	2/1997	511.86 -	1,756.92	1,661.79	04/2020 12/2020	12/2020
236	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483	4/2008	872.00 -	1,226.51	1,044.67	12/2019 10/2019	10/2019
237	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480	6/2018	229.00 -	860.92	39.69	12/2021 03/2023	03/2023
238	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420	9/2016	1,908.51 -	2,686.63	443.56	03/2023 03/2023	03/2023
239	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484	4/2015	1,973.00 -	1,973.66	139.42	03/2021 12/2022	12/2022
240	ANUPPUR-KATNI - [N22000485	4/2015	1,370.00 -	1,370.00	281.19	12/2021 12/2021	12/2021
	<u>South Eastern Railway</u>						
241	BOWAICHANDI-ARAMBAGH - [N22000159	4/2010	267.37 -	620.00	40.99	- 03/2025	03/2025
242	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL [N22000402	4/1998	1,027.40 -	2,373.00	485.04	03/2003 03/2030	03/2030
	<u>South Western Railway</u>						
243	YELAHANKA-PENUKONDA - [N22000328	5/2015	860.43 -	860.43	697.21	03/2020 -	03/2020
244	ARSIKERE-TUMKUR - [N22000332	3/2015	578.00 -	578.00	509.07	03/2020 -	03/2020
	<u>Southern Railway</u>						
245	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449	2/2015	1,700.00 -	1,003.00	167.73	03/2022 -	03/2022
	<u>Western Railway</u>						
246	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120	4/2008	3,503.69 -	3,860.40	1,676.43	03/2022 03/2023	03/2023
247	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM [N22000494	4/2017	691.84 -	663.29	166.84	03/2020 03/2021	03/2021
248	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493	4/2016	700.00 -	603.69	92.30	06/2020 06/2021	06/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
249	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487	2/1991	551.51 -	809.07	616.90	03/2019 03/2020	03/2020
250	SURENDRA NAGAR RAJKOT - [N22000392	4/2015	1,002.39 -	1,002.39	378.38	03/2021 03/2021	03/2021
251	VIRAMGAM-SAMAKHIALI (DL) - [N22000145	4/2011	1,037.15 -	1,037.15	992.18	03/2021 03/2022	03/2022
252	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143	4/1994	320.66 -	858.96	534.00	03/2019 03/2022	03/2022
253	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142	4/2011	844.10 -	844.10	97.74	- 03/2021	03/2021
254	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139	4/2007	1,640.04 -	1,640.04	682.91	03/2022 03/2023	03/2023
255	CHOTTAUDEPUR-DHAR(NL) - [N22000138	4/2007	1,347.26 -	1,347.26	724.63	03/2022 03/2022	03/2022
256	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123	4/2008	318.24 -	321.62	125.76	03/2012 03/2022	03/2022
257	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121	4/2008	829.74 -	1,310.23	1,394.73	03/2020 03/2021	03/2021
	Total		2,13,919.76 -	2,67,658.70	55,384.62		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways</u>						
258	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772	12/2017	257.34 -	257.34	62.79	12/2019 -	12/2019
259	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776	11/2017	232.81 -	232.81	59.44	11/2019 -	11/2019
260	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777	11/2017	283.51 -	283.51	126.38	11/2019 -	11/2019
261	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779	2/2018	418.88 -	418.88	88.00	02/2020 -	02/2020
262	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820	11/2017	237.80 -	238.00	7.48	11/2019 -	11/2019
263	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928	10/2015	333.21 -	355.89	265.48	12/2015 12/2019	12/2019
264	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO - [N24000930	11/2016	378.24 -	378.24	248.70	01/2018 01/2020	01/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
265	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932	1/2017	319.28 -	319.28	103.79	08/2017 03/2020	03/2020
266	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967	3/2016	444.84 -	444.84	234.31	09/2016 03/2020	03/2020
267	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964	8/2016	350.61 -	350.61	303.82	01/2017 12/2019	12/2019
268	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963	1/2018	418.03 -	418.03	144.09	08/2018 08/2020	08/2020
269	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940	3/2016	995.09 995.00	995.09	401.90	05/2016 03/2020	03/2020
270	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939	3/2018	504.19 504.00	504.19	201.11	11/2018 05/2020	05/2020
271	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938	3/2018	297.12 294.00	294.12	189.72	07/2018 01/2020	01/2020
272	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937	3/2018	289.67 290.00	289.67	80.77	08/2018 02/2020	02/2020
273	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU - [N24000936	3/2018	244.95 245.00	244.95	116.71	08/2018 02/2020	02/2020
274	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934	3/2018	228.32 -	228.32	34.74	08/2018 03/2020	03/2020
275	MAHAD TO RAIGAD FORT - [N24001038	7/2018	237.40 -	237.40	8.34	05/2020 -	05/2020
276	JAHIRABAD TO LATUR - [N24001040	1/2017	461.96 -	461.96	151.43	11/2019 -	11/2019
277	MANSAR TO SALAIKHURD - [N24001035	1/2018	418.36 -	418.36	116.13	12/2019 -	12/2019
278	PATGAON KHOPOLI SECTION I - [N24001028	1/2018	170.00 -	170.00	39.57	12/2019 -	12/2019
279	SHAHPUR PATGAON SECTION I - [N24001027	1/2018	150.79 -	150.79	21.42	12/2019 -	12/2019
280	KARASWADA TO BAMBOLIM - [N24001005	3/2017	852.67 -	852.67	108.04	12/2019 -	12/2019
281	PATRADEVI TO KARASWADA 4L - [N24001004	3/2017	634.32 -	634.32	102.33	05/2020 -	05/2020
282	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968	11/2016	376.25 -	376.25	196.09	08/2017 03/2020	03/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
283	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966	1/2016	348.95 -	348.95	161.18	08/2016 03/2020	03/2020
284	PARBHANI TO GANGKHED - [N24001065	3/2018	238.19 238.00	238.19	40.85	12/2019 -	12/2019
285	DHANGIPIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064	3/2018	217.14 217.00	217.14	66.77	02/2020 -	02/2020
286	WADIGODRI TO DHANGRIPIMPRI - [N24001063	3/2018	194.23 194.00	194.23	68.23	02/2020 -	02/2020
287	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062	3/2018	336.21 336.00	336.21	64.66	12/2019 -	12/2019
288	CHIKALI TO DHAD - [N24001061	3/2018	189.46 189.00	189.46	21.54	12/2019 -	12/2019
289	PALPHATA TO PHULAMBARI - [N24001060	3/2018	227.19 227.00	227.19	60.23	12/2019 -	12/2019
290	SHIVUR TO YEOLA - [N24001059	3/2018	181.08 -	181.08	2.50	12/2019 -	12/2019
291	KARWANDI TO RAJURI - [N24001058	3/2018	276.95 277.00	276.95	81.47	12/2019 -	12/2019
292	TASGAON TO SHIRDHON - [N24001054	1/2017	195.64 196.00	195.64	169.73	11/2019 -	11/2019
293	SELDOH TO PANVAR - [N24001097	7/2018	404.33 404.00	404.33	30.19	05/2020 -	05/2020
294	ARNI TO NAIGAINBANDI - [N24001093	12/2017	309.94 310.00	309.94	51.32	12/2019 -	12/2019
295	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091	3/2016	536.65 356.00	536.65	42.25	12/2019 -	12/2019
296	MALEGAON TO RISOD - [N24001089	2/2018	303.24 303.00	303.24	107.97	12/2019 -	12/2019
297	JALGAON TO NANDURA - [N24001088	3/2018	177.84 177.00	177.84	125.69	12/2019 -	12/2019
298	MANGRUPHIR TO MAHAN - [N24001087	3/2018	222.13 222.00	222.13	60.36	11/2019 -	11/2019
299	PAHUR TO BODHWAD - [N24001084	1/2017	244.93 -	244.93	40.23	05/2020 -	05/2020
300	CHIKLI TO TAKARKHED - [N24001083	3/2018	393.10 393.00	393.10	125.97	12/2019 -	12/2019
301	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082	3/2018	223.46 -	223.46	21.42	12/2019 -	12/2019
302	HIMAYATNAGAR TO PHULSAWANGI - [N24001081	3/2018	294.87 295.00	294.87	12.30	12/2019 -	12/2019
303	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080	3/2018	256.15 -	256.15	15.50	12/2019 -	12/2019
304	ARDHAPUR TO HIMAYATNAGAR - [N24001079	12/2017	426.06 426.00	426.06	66.97	06/2020 -	06/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
305	PUNE TO MALE VILLAGE - [N24001078]	3/2018	228.31 -	228.31	13.50	12/2019 -	12/2019
306	DEULGAON SAKARSHA TO MEHKAR - [N24001076]	3/2018	219.91 -	219.91	106.46	12/2019 -	12/2019
307	KUNDRAL TO WAZAR - [N24001077]	1/2018	225.25 225.00	225.25	121.75	12/2019 -	12/2019
308	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]	3/2018	249.29 -	249.29	72.20	12/2019 -	12/2019
309	OSMANNAGAR TO KUNDRAL - [N24001075]	9/2017	344.25 344.00	344.25	33.02	08/2020 -	08/2020
310	KOTHARI TO DHANORA - [N24001073]	9/2018	301.38 301.00	301.38	41.00	08/2020 -	08/2020
311	KHERDA TO NAGZARI - [N24001072]	3/2018	181.30 -	181.30	70.50	12/2019 -	12/2019
312	JALKOT TO TOGRI - [N24001071]	7/2018	299.92 300.00	299.92	4.20	08/2020 -	08/2020
313	DASTAPUR TO KARANJA - [N24001070]	3/2018	182.63 -	182.63	83.40	12/2019 -	12/2019
314	NANDED TO JALKOT - [N24001069]	12/2017	456.93 457.00	456.93	54.50	09/2019 -	09/2019
315	WASHIM TO DASTAPUR - [N24001068]	3/2018	165.51 -	165.51	35.45	12/2019 -	12/2019
316	OMREGA TO AUSA - [N24001067]	3/2018	272.04 272.00	272.04	124.24	12/2019 -	12/2019
317	LATUR TO PANGAON - [N24001066]	3/2018	336.47 336.00	336.47	109.48	12/2019 -	12/2019
318	SANGOLA TO JATH - [N24001052]	1/2018	257.38 257.00	257.38	61.15	12/2019 -	12/2019
319	NALDURG TO AKKALKOT - [N24001051]	2/2018	274.50 275.00	274.50	61.39	12/2019 -	12/2019
320	VITA TO NAGAJ - [N24001050]	3/2018	304.58 305.00	304.58	9.16	12/2019 -	12/2019
321	KARAD TO VITA - [N24001049]	1/2018	344.85 245.00	344.85	68.04	12/2019 -	12/2019
322	BHADGAON TO CHALISGAON - [N24001047]	1/2018	259.55 260.00	259.55	145.00	11/2019 -	11/2019
323	JALGAON TO BHADGAON - [N24001045]	1/2018	307.54 308.00	307.54	124.59	11/2019 -	11/2019
324	NILAJPHATA TO BHANDARA - [N24001043]	1/2018	420.63 421.00	420.63	17.60	05/2020 -	05/2020
325	SALAIKHURD TO TIRORA - [N24001042]	1/2018	415.25 415.25	415.25	82.22	12/2019 -	12/2019
326	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]	1/2019	264.50 -	264.50	-	03/2021 -	03/2021
327	WARDHA TO ARVI - [N24001150]	2/2018	313.58 -	313.58	4.96	04/2020 -	04/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
328	RISOD TO HINGOLI - [N24001149]	2/2018	355.99 -	355.99	112.97	12/2019 -	12/2019
329	KALMATH TO ZARAP - [N24001137]	9/2016	1,338.13 1,338.00	1,338.13	959.51	03/2020 -	03/2020
330	TALGAON TO KALMATH - [N24001136]	10/2016	904.70 905.00	904.70	604.05	03/2020 -	03/2020
331	KANTE TO WAKED - [N24001134]	3/2016	1,230.02 1,230.00	1,230.02	500.61	11/2019 -	11/2019
332	BHOGAN KHURD TO KASHEDI - [N24001132]	9/2017	743.21 743.00	743.21	131.87	06/2021 -	06/2021
333	NASRATPUR TO BARASGAON - [N24001112]	7/2016	406.54 407.00	406.54	142.00	09/2019 -	09/2019
334	BAMNI TO NAVAEGAON - [N24001110]	9/2017	241.69 242.00	241.69	146.29	04/2020 -	04/2020
335	KUSUMBA TO MALEGAON - [N24001109]	3/2018	243.45 244.00	243.45	67.02	12/2019 -	12/2019
336	CHALISGAON TO NANDGAON - [N24001108]	3/2018	206.97 207.00	206.97	78.89	12/2019 -	12/2019
337	PANCHARAL TO MANDANGHAR - [N24001107]	7/2018	381.08 302.00	381.08	13.00	05/2020 -	05/2020
338	WARDHA TO HINGAGHAT - [N24001098]	1/2018	216.90 217.00	216.90	45.00	12/2019 -	12/2019
339	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931]	11/2016	290.15 -	290.15	69.47	05/2017 03/2020	03/2020
340	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929]	9/2016	372.68 -	372.68	183.25	02/2017 12/2019	12/2019
341	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]	11/2017	257.34 -	238.00	41.09	11/2019 -	11/2019
342	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]	5/2018	248.00 -	248.00	-	05/2020 -	05/2020
343	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]	11/2017	266.52 -	266.52	144.27	11/2019 -	11/2019
344	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]	12/2017	200.34 -	200.34	31.00	12/2019 -	12/2019
345	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]	12/2017	248.22 -	248.22	57.20	12/2019 -	12/2019
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
346	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]	10/2014	369.00 -	369.00	308.97	03/2018 12/2019	12/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
347	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]	4/2017	428.11 -	428.11	-	09/2019 -	09/2019
348	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]	4/2017	404.29 -	404.29	-	09/2019 -	09/2019
349	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]	4/2017	518.53 -	518.53	-	09/2019 -	09/2019
350	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]	4/2017	537.82 -	537.82	-	09/2019 -	09/2019
351	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]	4/2017	473.18 -	473.18	-	09/2019 -	09/2019
352	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]	4/2017	642.96 -	642.96	-	09/2019 -	09/2019
353	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]	4/2017	640.07 -	640.07	-	09/2019 -	09/2019
354	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]	4/2017	519.09 -	519.09	-	09/2019 -	09/2019
355	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]	1/2016	252.00 -	252.00	4.74	01/2016 12/2021	12/2021
<u>National Highways Authority Of India</u>							
356	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]	10/2015	593.26 -	636.24	438.73	05/2018 06/2020	06/2020
357	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]	12/2015	649.50 -	649.50	134.58	03/2019 04/2021	04/2021
358	FOUR LANING OF SIMGA - SARAGAON - [N24000495]	12/2015	596.67 -	596.67	392.06	05/2018 10/2019	10/2019
359	NAGPUR RING ROAD PACKAGE-1 - [N24000558]	3/2016	546.00 -	546.00	269.67	07/2019 12/2020	12/2020
360	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]	8/2016	1,664.20 -	1,664.20	657.08	04/2020 -	04/2020
361	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]	3/2017	848.45 -	848.45	73.46	03/2020 -	03/2020
362	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	3/2017	672.89 -	736.01	-	03/2020 -	03/2020
363	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]	3/2018	291.53 -	291.53	30.82	- 11/2020	11/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
364	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814	3/2018	1,029.96 -	1,261.05	97.55	- 03/2021	03/2021
365	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	3/2017	2,064.99 -	2,447.00	1,653.62	03/2020 -	03/2020
366	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670	3/2017	239.68 -	235.90	91.24	03/2020 -	03/2020
367	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	3/2017	744.64 -	982.00	-	03/2020 -	03/2020
368	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599	8/2016	2,016.00 -	2,016.00	1,996.00	04/2019 11/2019	11/2019
369	NAGPUR RING ROAD PACKAGE-2 - [N24000560	3/2016	591.66 -	591.66	310.56	07/2019 12/2020	12/2020
370	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559	3/2016	720.00 -	720.00	285.96	- 10/2020	10/2020
371	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556	3/2016	899.00 -	899.00	532.53	04/2019 07/2020	07/2020
372	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551	3/2016	1,587.49 -	2,982.00	276.87	04/2019 10/2019	10/2019
373	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510	12/2015	726.67 -	598.13	414.73	04/2018 03/2020	03/2020
	<u>National Highways Development Project</u>						
374	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475	11/2015	628.45 -	628.45	252.21	01/2020 -	01/2020
375	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478	12/2015	957.54 -	957.54	467.50	02/2020 -	02/2020
	<u>Public Works Dept Of State</u>						
376	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301	3/2015	271.45 -	271.45	152.90	10/2015 11/2019	11/2019
377	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880	2/2018	426.18 -	426.18	219.94	09/2020 -	09/2020
378	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882	2/2018	218.70 -	218.70	37.75	11/2020 -	11/2020
379	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879	3/2017	202.69 -	202.69	93.93	11/2019 -	11/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
380	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874	3/2016	271.17 291.20	291.20	80.26	11/2018 11/2019	11/2019
381	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883	3/2018	254.30 -	254.30	52.85	10/2020 -	10/2020
382	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905	3/2018	322.48 -	322.48	48.73	07/2020 -	07/2020
383	REHABILITATION AND UPGRADATION OF ALLAHABAD - MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203	10/2016	218.90 -	218.90	23.37	03/2020 -	03/2020
384	REHABILITATION AND UPGRADATION OF BARAICH - SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA - [N24001202	3/2016	388.83 -	388.83	280.17	12/2019 -	12/2019
385	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197	3/2018	351.00 -	351.00	.48	06/2021 -	06/2021
386	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180	3/2019	237.51 -	237.51	-	12/2022 -	12/2022
387	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMIONG TO UNGER) ON MOKOKCHUN - [N24001179	3/2017	217.35 -	217.35	35.10	11/2020 -	11/2020
388	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178	11/2016	336.25 -	336.25	62.64	09/2019 -	09/2019
389	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177	10/2016	171.90 -	171.90	11.75	08/2020 -	08/2020
390	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176	10/2016	172.63 -	172.63	45.02	12/2020 -	12/2020
391	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175	10/2016	167.62 -	167.62	42.15	12/2020 -	12/2020
392	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209	3/2016	296.50 -	296.50	.51	09/2020 -	09/2020
393	FOUR LANING WIDENING & STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (JAN - [N24001208	3/2018	288.30 -	288.30	.34	08/2020 -	08/2020
394	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207	3/2018	185.18 -	185.18	2.86	02/2020 -	02/2020
395	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206	3/2018	263.89 -	263.89	67.69	04/2020 -	04/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
396	R AND U FROM KM 385.00 TO KM 420.000 TO 2- LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404 - [N24001205	12/2016	209.10 -	209.10	54.18	10/2019 -	10/2019
397	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204	7/2016	208.88 -	208.88	36.25	10/2019 -	10/2019
398	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. - [N24001174	10/2016	235.31 -	235.31	91.38	11/2020 -	11/2020
399	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152	9/2018	160.00 -	160.00	.50	09/2021 -	09/2021
400	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148	3/2016	599.34 -	599.34	449.19	01/2020 -	01/2020
401	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141	3/2016	240.30 240.00	240.30	194.01	01/2020 -	01/2020
402	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140	11/2016	215.16 215.00	215.16	157.79	09/2019 -	09/2019
403	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA - [N24001139	10/2016	218.94 219.00	218.94	86.07	03/2020 -	03/2020
404	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131	3/2018	212.99 -	212.99	80.47	06/2020 -	06/2020
405	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984	1/2017	283.00 -	283.00	152.35	12/2019 -	12/2019
406	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983	1/2017	196.52 -	196.52	103.12	10/2019 -	10/2019
407	REHABILITATION AND UPGRADATION OF HARPALPUR-SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942	3/2016	208.50 -	208.50	123.66	11/2019 -	11/2019
408	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941	3/2018	293.64 -	293.64	28.24	08/2020 -	08/2020
409	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927	3/2018	293.64 -	293.64	28.24	08/2020 -	08/2020
410	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910	3/2018	170.57 -	170.57	46.23	11/2020 -	11/2020
411	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909	10/2017	1,069.59 -	1,069.59	629.87	10/2019 -	10/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
412	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907	3/2018	293.10 -	293.10	10.26	08/2020 -	08/2020
413	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906	3/2018	173.24 -	173.24	10.97	06/2020 -	06/2020
414	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996	1/2017	605.08 -	605.08	273.88	10/2019 -	10/2019
415	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994	3/2018	626.76 -	626.76	80.66	07/2020 -	07/2020
416	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993	3/2018	322.81 -	322.81	1.66	09/2020 -	09/2020
417	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992	2/2018	426.52 -	426.52	225.51	04/2020 -	04/2020
418	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991	2/2018	220.28 -	220.28	37.58	11/2019 -	11/2019
419	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990	2/2018	294.13 -	294.13	39.44	11/2019 -	11/2019
420	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989	2/2018	206.13 -	206.13	127.86	06/2020 -	06/2020
421	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988	1/2018	230.03 -	230.03	127.98	12/2019 -	12/2019
422	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987	1/2018	283.15 -	283.15	42.22	05/2020 -	05/2020
423	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C - [N24000999	11/2016	230.34 -	230.34	178.39	10/2019 -	10/2019
424	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884	3/2018	191.21 -	191.21	72.02	11/2019 -	11/2019
	Total		67,545.58 -	69,784.90	23,058.51		
	<u>SHIPPING AND PORTS</u>						
	<u>Inland Waterways Authority Of India</u>						
425	JAL MARG VIKAS PROJECT - [N25000072	1/2018	4,200.00 -	5,369.18	1,400.95	03/2023 03/2023	03/2023
	Total		4,200.00 -	5,369.18	1,400.95		

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmdc)</u>						
426	NMDC INTEGRATED STEEL PLANT - [N12000086]	1/2010	15,525.00 -	23,140.00	16,064.29	05/2015 07/2020	07/2020
	<u>Rastriya Ispat Nigam Limited</u>						
427	FORGED WHEEL PLANT - [N12000116]	4/2014	1,682.85 -	1,682.85	1,227.53	09/2018 10/2019	10/2019
428	COKE OVEN BATTERY-5 - [N12000117]	12/2011	2,858.00 -	2,500.00	1,400.76	12/2017 10/2019	10/2019
429	CENTRAL DISPATCH YARD - [N12000119]	8/2015	320.66 -	320.66	220.91	08/2018 10/2019	10/2019
	<u>Steel Authority Of India Limited (Sail)</u>						
430	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]	4/2015	3,127.30 -	3,127.30	3,031.06	04/2018 11/2019	11/2019
431	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]	3/2015	1,034.01 -	1,034.01	436.08	10/2017 06/2020	06/2020
432	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E - [N12000121]	12/2018	263.36 -	263.36	11.32	09/2020 -	09/2020
433	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]	5/2015	1,154.18 -	1,154.18	963.95	12/2017 11/2019	11/2019
434	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]	11/2016	262.87 -	262.87	104.85	06/2019 06/2020	06/2020
	Total		26,228.23 -	33,485.23	23,460.75		
	<u>TELECOMMUNICATIONS</u>						
	<u>Bharat Sanchar Nigam Limited</u>						
435	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]	1/2018	231.80 -	240.10	117.63	10/2018 12/2019	12/2019
	Total		231.80 -	240.10	117.63		
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
436	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]	11/2017	238.56 -	238.56	63.42	05/2020 -	05/2020
437	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]	10/2017	271.90 -	271.90	33.56	11/2019 -	11/2019
438	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]	1/2018	223.37 -	223.37	33.01	07/2020 09/2020	09/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(September 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
439	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]	1/2019	790.79 -	800.00	2.56	03/2022 -	03/2022
440	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST) - [N28000112]	9/2017	150.29 -	150.29	2.58	03/2020 -	03/2020
441	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]	11/2017	171.72 -	171.72	32.00	03/2020 -	03/2020
	<u>Maharashtra Metro Rail Corporation Ltd.</u>						
442	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]	12/2016	11,420.00 -	11,420.00	2,896.26	11/2021 01/2022	01/2022
	<u>Madhya Pradesh Metro Rail Co Limited</u>						
443	BHOPAL METRO RAIL - [N28000124]	11/2018	6,941.40 -	6,941.40	34.12	02/2023 -	02/2023
444	INDORE METRO RAIL - [N28000125]	11/2018	7,500.80 -	7,500.80	42.62	02/2023 -	02/2023
	<u>National Building Construction Corporation Ltd</u>						
445	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,439.23	3,246.53	11/2019 -	11/2019
	Total		31,972.83 -	32,157.27	6,386.66		
	<u>WATER RESOURCES</u>						
	<u>Brahmaputra Board</u>						
446	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]	3/2017	233.57 -	233.57	32.20	12/2019 -	12/2019
	Total		233.57 -	233.57	32.20		
	Grand Total		7,32,625.33	8,24,780.34	2,91,616.71		

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Annexure - XIII

Costing Rs. 150 Crore and above					(September 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,840.00	09/2010 -	10/2021	95.88
	Total		3,492.00 -	6,840.00			
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI [N04000083]	12/2016	859.86 -	860.00	03/2021 -	03/2021	.02
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]	09/2015	338.93 -	339.00	06/2019 -	12/2019	.02
	Total		1,513.40 -	1,640.33			
	<u>COAL</u>						
	<u>Eastern Coal Fields Limited</u>						
5	RANIGANJ MASTER PLAN - [N06000163]	08/2009	2,661.73 -	5,186.24	08/2019 -	-	94.84
	<u>Neyveli Lignite Corporation</u>						
6	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80	11/2021 -	11/2021	.00
	<u>Singareni Colliers Company Limited</u>						
7	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86
8	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	03/2012 -	03/2024	80.24
9	KAKATIYAKHANI OPENCASE-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	03/2019 -	03/2020	11.42
10	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 -	473.22	03/2015 -	03/2021	5.85
11	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	03/2015 -	03/2021	114.60
	<u>South-Eastern Coal Fields Limited</u>						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(September 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
12	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43	459.49	03/2015	03/2020	201.44
	<u>Western Coal Fields Limited</u>						
13	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65	313.34	03/2021	03/2024	12.85
14	BHANEGAON OC - [N06000121]	02/2015	187.94	409.68	03/2023	03/2023	117.98
15	ADASA UG TO OC - [N06000133]	08/2015	288.90	333.43	03/2023	03/2024	15.41
	Total		22,480.56	26,143.38			
	<u>FERTILISERS</u>						
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
16	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79	209.44	11/2016	09/2019	5.89
	Total		197.79	209.44			
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation Ltd</u>						
17	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	02/2013	414.11	513.89	11/2013	10/2020	24.10
18	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	09/2014	505.58	523.00	03/2018	-	3.45
19	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]	12/2017	156.56	156.65	-	02/2020	.06
	Total		1,076.25	1,193.54			
	<u>PETROLEUM</u>						
	<u>Gas Authority Of India Limited</u>						
20	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	02/2015	749.00	842.00	02/2020	02/2020	12.42
21	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]	06/2009	2,915.00	3,049.47	12/2012	02/2022	4.61
	<u>Hindustan Petroleum Corporation Limited</u>						
22	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]	11/2011	310.00	370.00	03/2013	-	19.35
	<u>Indian Oil Corporation Limited</u>						
23	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06	714.25	10/2017	-	17.66

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(September 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>Indian Strategic Petroleum Reserves Ltd</u>						
24	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00	1,693.00	01/2012	-	70.49
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
25	SEA WATER DESALINATION PLANT - [N16000319]	11/2017	581.00	621.00	03/2020	09/2020	6.88
	<u>Oil & Natural Gas Corporation Limited</u>						
26	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79	1,683.06	05/2013	12/2019	95.30
27	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69	3,247.19	04/2018	05/2020	1.77
28	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]	02/2017	968.61	1,033.95	11/2019	11/2019	6.75
29	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]	02/2017	4,006.83	4,475.92	05/2021	12/2021	11.71
	<u>Oil India Limited</u>						
30	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56	438.84	03/2017	12/2019	24.47
31	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35	1,200.00	03/2015	-	37.72
32	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	01/2018	543.91	682.90	02/2020	06/2020	25.55
	Total		16,950.80	20,051.58			
	<u>POWER</u>						
	<u>National Hydro-Electric Power Corporation</u>						
33	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59	9,997.11	09/2009	12/2021	155.06
34	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33	19,496.34	09/2010	-	210.19
	<u>National Thermal Power Corporation</u>						
35	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55	12,865.92	01/2018	03/2020	10.55
36	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44	13,740.53	12/2018	09/2020	9.64
37	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58	15,164.05	06/2019	09/2021	5.55

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(September 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
38	RAMMAM-III HEPP (3X40 MW) - [N18000178]	09/2014	1,381.84 -	1,592.34	09/2019 -	02/2022	15.23
39	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	9,996.59	07/2012 -	09/2020	86.75
40	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]	04/2012	9,750.89 -	12,176.28	02/2017 -	06/2020	24.87
41	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	10/2017 -	03/2020	7.55
42	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	07/2012	1,527.00 -	1,801.07	08/2017 -	-	17.95
43	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	03/2015	9,870.51 -	11,148.86	01/2020 -	01/2020	12.95
44	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	10/2017 -	-	7.41
<u>Power Grid Corporation Of India Limited</u>							
45	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]	10/2008	4,824.12 -	5,071.94	10/2012 -	12/2019	5.14
46	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	14,719.10	08/2013 -	03/2022	32.24
47	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	04/2016 -	11/2019	38.61
48	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	546.36	11/2016 -	03/2020	4.61
49	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	02/2014	196.58 -	225.28	02/2016 -	06/2019	14.60
50	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP - [N18000180]	01/2015	268.80 -	340.88	03/2018 -	06/2019	26.82
51	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03	07/2017 -	10/2019	27.92
52	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	06/2014 -	10/2019	31.17
53	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,187.32	11/2008 -	-	22.93
54	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,072.36	12/2018 -	12/2020	90.82
55	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,880.36	12/2018 -	12/2020	34.61
<u>Thdc India Limited</u>							
56	DHUKWAN SMALL HYDRO PROJECT - [N18000189]	05/2011	195.42 -	294.60	02/2014 -	12/2019	50.75
57	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	4,397.80	06/2013 -	12/2022	76.51

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(September 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
58	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	5,024.35	02/2016 -	06/2022	203.22
	Total		1,27,696.00 -	1,76,822.16			
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
59	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89 -	1,377.48	03/2021 -	03/2022	73.73
60	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 -	305.00	03/2019 -	12/2019	65.71
61	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 -	3,712.50	03/2021 -	03/2022	63.44
62	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 -	5,341.68	03/2024 -	03/2024	120.28
63	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 -	3,438.51	03/2024 -	03/2024	25.04
64	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	02/2015	3,627.47 3,627.00	3,627.47	03/2024 -	03/2022	.01
65	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	03/2023 -	03/2023	10.94
	<u>Container Corporation Of India</u>						
66	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 -	235.00	03/2019 -	12/2020	.21
	<u>East Central Railways</u>						
67	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]	03/1999	1,033.07 -	3,376.00	- -	03/2021	226.79
68	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	04/1997	324.73 -	1,050.00	03/2012 -	03/2020	223.35
69	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 -	549.75	- -	-	32.26
70	BIHTA-AURANGABAD (NL) - [N22000170]	04/2008	326.20 -	2,995.01	- -	03/2024	818.15
71	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	378.56 -	2,609.00	- -	03/2022	589.19
72	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	1,006.00	- -	-	376.78
73	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC [N22000181]	04/2009	548.00 -	819.01	03/2020 -	03/2022	49.45
74	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	425.17	- -	01/2020	99.60
75	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN- BIHARSHARIF, - [N22000476]	04/1991	329.39 -	1,483.14	- -	12/2021	350.27

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(September 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>East Coast Railway</u>						
76	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	810.78 -	1,928.07	06/2021 -	06/2024	137.80
77	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	2,923.13 -	3,791.66	03/2009 -	06/2024	29.71
78	SAMBALPUR-TALCHER DOUBLING - [N22000315	03/2011	1,111.99 -	1,539.28	02/2019 -	03/2022	38.43
79	KIRANDUL - JAGDALPUR DOUBLING - [N22000318	12/2012	1,160.00 -	1,160.83	03/2020 -	03/2023	.07
80	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319	03/2012	155.81 -	238.03	03/2020 -	03/2021	52.77
81	KOTTAVALSA - KORAPUT DOUBLING - [N22000377	04/2015	2,499.71 -	3,382.95	03/2022 -	03/2022	35.33
82	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE [N22000380	04/2015	701.61 -	810.02	11/2018 -	03/2022	15.45
	<u>Eastern Railways</u>						
83	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	1,188.91 -	1,619.48	03/2019 12/2009	03/2025	36.22
84	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	607.09 -	1,425.44	02/2013 -	03/2024	134.80
85	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235	04/2010	365.17 -	527.54	- -	03/2025	44.46
86	HANSDIHA-GODDA NL - [N22000236	04/2011	542.18 -	693.80	03/2020 -	03/2021	27.96
87	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238	04/2011	175.80 -	245.41	- -	03/2021	39.60
88	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239	04/2011	299.60 -	335.62	03/2017 -	03/2026	12.02
89	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI- BAHRAHAT NL - [N22000240	04/2010	494.54 -	494.59	03/2005 -	03/2025	.01
90	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR- MINAKHAN VIA GHATAKPUR NL [N22000241	04/2000	297.47 -	298.22	- -	03/2025	.25
91	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243	04/2009	499.96 -	680.68	02/2012 -	03/2025	36.15
92	MONIGRAM- NIMTITA - [N22000301	04/2012	250.93 -	310.70	- -	03/2024	23.82
93	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302	04/2012	255.64 -	272.20	- -	09/2021	6.48
94	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP- BUDAKHALI AND CHANDRANAG - [N22000216	04/1987	406.99 -	545.70	03/2006 -	03/2025	34.08

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(September 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
95	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]	04/2007	450.00 -	1,261.34	-	03/2025	180.30
96	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 -	260.10	-	03/2025	51.19
97	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	2,137.81	03/2022 -	03/2025	133.39
98	BANDEL-BOINCHI 3RD LINE - [N22000221]	04/2011	288.35 -	382.90	-	03/2020	32.79
99	PIRPAINTI-BHAGALPUR - [N22000222]	04/2011	261.38 -	471.81	-	05/2019	80.51
100	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]	04/2001	923.52 -	995.10	03/2016 -	03/2025	7.75
101	CHINPAI- SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]	04/2005	595.51 -	769.40	03/2017 -	03/2025	29.20
	<u>Indian Railway Construction Company Limited</u>						
102	GEVRA ROAD PENDRA ROAD - [N22000488]	02/2014	2,288.00 -	4,970.11	03/2022 -	12/2022	117.23
	<u>Metropolitan Rapid Transport Projects</u>						
103	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
104	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	2,980.41	03/2004 -	03/2021	501.57
105	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 -	734.01	06/2013 -	-	48.06
106	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	03/2013	4,874.58 -	8,574.97	03/2016 -	06/2021	75.91
	<u>North Central Railway</u>						
107	ETAWAH-MAINPURI (NL),NCR - [220100318]	04/1997	120.00 -	346.00	12/2008 -	-	188.33
108	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96 -	3,845.60	03/2022 -	12/2024	32.02
109	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	04/2015	668.70 668.00	680.00	03/2020 -	03/2020	1.80
	<u>North East Frontier Railway</u>						
110	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	297.32 -	614.00	03/2019 -	03/2020	106.51
111	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 -	5,021.45	03/2014 -	03/2022	109.80
112	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	1,180.19 -	4,541.00	12/2008 -	03/2021	284.77

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(September 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
113	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	2,326.52	4,600.00	03/2015	10/2021	97.72
114	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	333.76	360.00	-	03/2022	7.86
115	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48	4,084.69	12/2015	-	204.95
116	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00	2,496.67	03/2019	-	38.86
117	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42	380.00	-	03/2022	71.62
118	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63	650.00	03/2020	12/2021	14.11
119	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	906.46	6,000.00	03/2021	03/2021	561.92
120	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22	471.00	03/2020	03/2020	94.45
121	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52	394.28	-	03/2021	63.25
122	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84	661.00	03/2020	03/2020	59.34
123	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	04/1999	819.23	1,871.00	-	-	128.39
124	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96	2,136.01	03/2021	03/2021	145.25
125	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	04/2016	602.27	612.00	12/2021	03/2020	1.62
126	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHOWA-JAIN - [N22000499]	02/1999	380.60	1,871.00	04/2010	-	391.59
<u>North Eastern Railway</u>							
127	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	142.45	228.40	-	-	60.34
128	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92	197.73	-	-	8.10
129	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00	1,409.09	-	-	358.99
130	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78	895.00	12/2021	12/2021	267.13
131	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00	477.31	01/2019	01/2020	61.80
132	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00	644.00	-	-	.16

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(September 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
133	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	04/2016 -	06/2020	.16
134	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]	04/2017	1,343.00 -	1,476.15	01/2018 -	-	9.91
135	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]	04/2016	602.50 -	714.34	- -	-	18.56
	<u>North Western Railway</u>						
136	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	886.41	02/2019 -	03/2021	116.16
137	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	685.99	03/2020 -	04/2022	14.33
138	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL [N22000330]	05/2015	873.71 -	1,980.21	- -	-	126.64
139	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	348.55	12/2019 -	06/2020	41.64
140	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	4,079.15	- -	-	95.85
141	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	294.90	10/2018 -	10/2019	24.47
142	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]	04/2013	822.00 -	1,099.54	- -	-	33.76
143	PUSHKAR-MERTA - [N22000151]	04/2013	323.00 -	432.22	- -	-	33.81
144	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	303.56	11/2019 -	05/2020	42.26
145	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	410.00	02/2019 -	05/2020	69.36
	<u>Northern Railway</u>						
146	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	197.17	- -	03/2024	25.87
147	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	694.00	12/2011 -	03/2021	141.81
148	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]	04/2007	336.91 -	800.00	- -	03/2022	137.45
149	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63	- -	06/2020	57.68
150	UNCHAHAAR-AMETHI - [N22000294]	04/2012	1,229.00 -	1,230.00	- -	03/2023	.08
151	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,010.00	07/2012 -	03/2024	346.67
152	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 -	1,540.00	03/2023 -	03/2023	369.31
153	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 -	845.58	03/2016 -	03/2021	35.29

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(September 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>Rail Vikas Nigam Ltd.</u>						
154	HARIDASPUR-PARADEEP(NL) - [N220100285]	04/1996	1,185.64 -	1,844.47	12/2017 -	03/2020	55.57
155	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [N220100327]	04/2000	133.41 207.00	385.00	03/2009 03/2009	12/2019	85.99
156	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	2,966.99 -	7,000.00	12/2026 -	12/2025	135.93
157	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 -	2,900.00	03/2023 -	03/2024	36.34
158	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2025	7.78
159	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95
160	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	975.62 -	1,082.32	12/2021 -	12/2021	10.94
161	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2020	29.06
162	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.67	12/2023 -	12/2023	9.32
163	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,200.00	03/2019 -	03/2020	29.45
164	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 -	1,950.00	03/2020 -	03/2020	173.31
165	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 -	2,335.68	12/2024 -	12/2024	.00
166	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 -	1,500.00	03/2020 -	03/2021	58.22
167	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 -	1,120.00	03/2019 -	06/2022	18.78
	<u>Railway Electrification</u>						
168	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	-	60.77
	<u>South Central Railway</u>						
169	KOTLPALLI-NARASAPUR (NL) (SCR) - [N220100265]	12/2001	1,045.20 -	2,120.16	03/2009 -	03/2023	102.85
170	MANUGURU-RAMAGUNDAM - [N22000259]	04/2013	1,112.00 -	2,911.84	- -	-	161.86
171	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,856.95 -	2,200.00	03/2023 -	03/2024	18.47
172	BHADRACHALAM-KOVVUR - [N22000264]	04/2012	923.23 -	1,787.00	- -	-	93.56

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(September 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
173	CUMBUM-PRODDATUR - [N22000282]	04/2013	829.00 -	1,599.39 -	- -	- -	92.93
174	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	704.31 -	1,352.74 -	03/2020 -	03/2020 -	92.07
175	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	164.36 -	1,050.00 -	02/2009 -	- -	538.84
176	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	1,723.00 1.00	1,723.00 -	03/2000 -	03/2021 -	1,72,200.00
177	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	458.25 -	458.26 -	- -	- -	.00
178	KONDAPALLI-KOTHAGUEDEM - [N22000364]	04/2013	723.00 -	997.09 -	- -	- -	37.91
	<u>South East Central Railway</u>						
179	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	1,413.76 -	- -	10/2019 -	268.37
180	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438]	04/2010	585.93 -	1,300.44 -	02/2019 -	06/2020 -	121.94
181	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00 -	860.92 -	12/2021 -	03/2023 -	275.95
	<u>South Eastern Railway</u>						
182	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00 -	03/2007 03/2007	- -	564.94
183	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	377.00 -	12/2016 -	12/2019 -	153.41
184	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	620.00 -	- -	03/2025 -	131.89
185	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	651.00 -	1,009.00 -	03/2015 -	- -	54.99
186	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00 -	03/2015 -	- -	53.44
187	BONDAMUNDA RANCHI DOUBLING - [N22000396]	03/2016	1,724.20 -	1,993.24 -	03/2021 -	12/2021 -	15.60
188	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 -	2,373.00 -	03/2003 -	03/2030 -	130.97
	<u>South Western Railway</u>						
189	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43 -	- -	12/2023 -	24.09
190	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65 -	- -	12/2023 -	57.65
191	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50 -	- -	12/2023 -	14.14
192	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77 -	- -	12/2023 -	12.38

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(September 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
193	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 -	1,870.41	03/2019 -	03/2021	15.84
194	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78 -	889.52	03/2017 -	03/2020	37.96
	<u>Southern Railway</u>						
195	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY'-AGASTIYAMPALLI [N22000079]	09/2007	724.69 -	2,072.50	02/2019 -	02/2020	185.98
196	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	227.40 -	900.00	- -	-	295.78
197	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	582.83 -	2,300.00	- -	-	294.63
198	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	303.98 -	980.00	03/2020 -	03/2021	222.39
199	ATTIPPATTU PUTTUR - [N22000184]	04/2008	151.84 -	1,105.00	02/2019 -	-	627.74
200	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	2,300.00	- -	-	339.33
201	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
202	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17
203	ERODE-PALANI - [N22000199]	04/2008	288.57 -	1,140.00	- -	-	295.05
204	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	03/2020	173.71
205	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	931.98 -	951.24	- -	03/2020	2.07
206	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215]	04/2011	120.70 -	1,800.00	03/2019 -	12/2019	1,391.30
207	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM [N22000373]	10/2013	187.26 -	231.67	04/2014 -	03/2020	23.72
208	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	02/1996	268.87 -	950.00	03/2005 -	-	253.33
209	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00 -	1,182.31	03/2020 -	06/2021	55.57
	<u>West Central Railway</u>						
210	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60 -	2,909.99	03/2021 -	03/2023	585.35
211	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35
212	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13 -	1,247.64	03/2022 -	09/2022	114.32

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(September 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>Western Railway</u>						
213	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	3,503.69 -	3,860.40	03/2022 -	03/2023	10.18
214	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]	04/2006	117.36 196.95	202.35	03/2011 -	03/2017	2.74
215	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	04/2008	829.74 -	1,310.23	03/2020 -	03/2021	57.91
216	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	858.96	03/2019 -	03/2022	167.87
	Total		1,32,336.65 -	2,47,460.54			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Dept Of Road Transport & Highways</u>						
217	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]	03/2015	280.16 -	290.59	- -	-	3.72
	<u>Ministry Of Road Transport And Highways</u>						
218	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]	12/2011	156.26 227.00	247.95	- -	-	9.23
219	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]	03/2015	258.97 -	268.92	08/2015 -	-	3.84
220	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]	01/1991	675.00 -	780.77	- -	-	15.67
221	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]	01/1991	282.41 -	322.01	08/2016 -	-	14.02
222	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]	01/1991	358.22 -	377.64	10/2016 -	-	5.42
223	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]	06/2016	157.30 157.00	157.30	06/2018 -	-	.19
224	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]	03/2018	460.73 -	461.00	- -	-	.06
225	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]	11/2017	237.80 -	238.00	11/2019 -	11/2019	.08
226	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DSIGN CH0.0) TO KM 275/622(DSIGN CH 5.12 - [N24000928]	10/2015	333.21 -	355.89	12/2015 -	12/2019	6.81

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(September 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
227	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938	03/2018	297.12 294.00	294.12	07/2018 -	01/2020	.04
228	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939	03/2018	504.19 504.00	504.19	11/2018 -	05/2020	.04
229	REHABILITATION AND UPGRADATION OF KARNATAKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940	03/2016	995.09 995.00	995.09	05/2016 -	03/2020	.01
230	KHAMGAON TO SHEGAON - [N24001009	02/2017	203.21 203.00	203.21	05/2019 -	12/2019	.10
231	SHEGAON TO DEORI PHATA - [N24001010	02/2017	373.10 373.00	373.10	05/2019 -	12/2019	.03
232	MEHKAR TO CHIKALI - [N24001011	02/2017	322.48 322.00	322.48	05/2019 -	-	.15
233	CHIKALI TO KHAMGAON - [N24001012	02/2017	548.03 548.00	548.03	06/2019 -	10/2019	.01
234	DIGRAS DARWAH KARANJA - [N24001013	01/2017	391.06 391.00	391.06	06/2019 -	06/2020	.02
235	MORSHI TO ACHALPUR - [N24001015	01/2017	341.16 341.00	341.16	06/2019 -	12/2019	.05
236	KARAD TO VITA - [N24001049	01/2018	344.85 245.00	344.85	12/2019 -	12/2019	40.76
237	SANGOLA TO JATH - [N24001052	01/2018	257.38 257.00	257.38	12/2019 -	12/2019	.15
238	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056	02/2017	422.02 422.00	422.02	07/2019 -	-	.00
239	KARAD PATAN CHIPLUN GUHAGAR - [N24001057	02/2017	407.19 407.00	407.19	06/2019 -	06/2020	.05
240	PALPHATA TO PHULAMBARI - [N24001060	03/2018	227.19 227.00	227.19	12/2019 -	12/2019	.08
241	CHIKALI TO DHAD - [N24001061	03/2018	189.46 189.00	189.46	12/2019 -	12/2019	.24
242	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062	03/2018	336.21 336.00	336.21	12/2019 -	12/2019	.06
243	WADIGODRI TO DHANGRIIMPRI - [N24001063	03/2018	194.23 194.00	194.23	02/2020 -	02/2020	.12
244	DHANGRIIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064	03/2018	217.14 217.00	217.14	02/2020 -	02/2020	.06
245	PARBHANI TO GANGKHED - [N24001065	03/2018	238.19 238.00	238.19	12/2019 -	12/2019	.08
246	LATUR TO PANGAON - [N24001066	03/2018	336.47 336.00	336.47	12/2019 -	12/2019	.14
247	OMREGA TO AUSA - [N24001067	03/2018	272.04 272.00	272.04	12/2019 -	12/2019	.01

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(September 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
248	KOTHARI TO DHANORA - [N24001073]	09/2018	301.38 301.00	301.38	08/2020 -	08/2020	.13
249	OSMANNAGAR TO KUNDRAL - [N24001075]	09/2017	344.25 344.00	344.25	08/2020 -	08/2020	.07
250	KUNDRAL TO WAZAR - [N24001077]	01/2018	225.25 225.00	225.25	12/2019 -	12/2019	.11
251	ARDHAPUR TO HIMAYATNAGAR - [N24001079]	12/2017	426.06 426.00	426.06	06/2020 -	06/2020	.01
252	JALGAON TO NANDURA - [N24001088]	03/2018	177.84 177.00	177.84	12/2019 -	12/2019	.47
253	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]	03/2016	536.65 356.00	536.65	12/2019 -	12/2019	50.74
254	NAIGAONBANDI TO MANGRULPIR - [N24001094]	12/2017	244.04 244.00	244.04	03/2019 -	12/2019	.02
255	TALEGAON TO GONAPUR - [N24001096]	01/2018	264.41 264.00	264.41	03/2019 -	12/2019	.16
256	SELDOH TO PANVAR - [N24001097]	07/2018	404.33 404.00	404.33	05/2020 -	05/2020	.08
257	PANCHARAL TO MANDANGHAR - [N24001107]	07/2018	381.08 302.00	381.08	05/2020 -	05/2020	26.19
258	BHOKAR TO SARSAM - [N24001128]	02/2017	295.09 -	295.99	07/2019 -	-	.31
259	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]	10/2013	445.89 653.00	653.29	03/2017 -	09/2019	.04
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
260	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]	03/2016	396.52 -	396.52	08/2016 -	06/2020	.00
261	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]	03/2016	429.52 -	429.52	08/2016 -	08/2019	.00
262	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]	04/2017	388.00 -	447.37	10/2017 -	-	15.30
263	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]	03/2018	339.57 -	339.57	09/2018 -	-	.00
264	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]	03/2018	237.72 -	237.72	09/2018 -	-	.00
265	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]	03/2018	251.97 -	251.97	09/2018 -	-	.00
	<u>National Highways Authority Of India</u>						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(September 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
266	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [N240106277]	12/2003	280.00 -	525.00	02/2009 -	07/2019	87.50
267	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]	12/2003	160.00 -	167.98	05/2008 -	06/2019	4.99
268	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61 -	360.84	04/2010 -	07/2019	65.82
269	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 -	230.00	04/2008 -	03/2020	10.58
270	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	2,945.00	04/2015 -	-	52.73
271	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]	10/2015	531.13 -	727.00	05/2018 -	09/2020	36.88
272	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]	10/2015	593.26 -	636.24	05/2018 -	06/2020	7.24
273	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]	06/2015	845.24 -	941.00	- -	10/2019	11.33
274	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	05/2013	1,055.00 -	1,601.77	11/2015 -	-	51.83
275	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]	07/2015	1,871.34 -	1,871.34	01/2018 -	12/2019	.00
276	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 TO 208.300 KM [PACKAGE-IV] - [N24000551]	03/2016	1,587.49 -	2,982.00	04/2019 -	10/2019	87.84
277	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]	05/2016	425.60 -	425.60	- -	-	.00
278	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]	05/2016	364.56 -	392.00	- -	12/2019	7.53
279	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]	09/2015	771.18 -	7,558.00	- -	-	880.06
280	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]	09/2016	950.69 -	1,108.00	08/2019 -	12/2020	16.55
281	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]	11/2012	605.84 -	722.46	07/2018 -	02/2020	19.25
282	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	03/2017	1,184.71 -	1,310.00	03/2020 -	08/2020	10.58
283	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	03/2017	744.64 -	982.00	03/2020 -	03/2020	31.88
284	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	03/2017	1,030.44 -	1,065.51	03/2020 -	05/2020	3.40
285	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	03/2017	988.34 -	1,043.28	03/2020 -	08/2020	5.56

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(September 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
286	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	03/2017	1,098.06 -	1,160.64	03/2020 -	08/2020	5.70
287	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	03/2017	754.54 -	756.27	03/2020 -	04/2020	.23
288	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	03/2017	672.89 -	736.01	03/2020 -	03/2020	9.38
289	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 -	1,187.10	03/2020 -	05/2020	13.97
290	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669	03/2017	165.50 -	172.16	03/2020 -	-	4.02
291	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 -	1,420.00	03/2020 -	03/2021	10.24
292	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 -	2,447.00	03/2020 -	03/2020	18.50
293	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 -	1,177.00	03/2020 -	07/2020	41.54
294	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	03/2020 -	06/2020	44.39
295	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704	09/2017	1,124.11 -	1,232.76	09/2017 -	06/2020	9.67
296	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730	01/2018	621.00 -	621.00	-	04/2021	.00
297	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784	02/2018	1,424.77 -	1,853.42	-	-	30.09
298	SIX-LANING OF BANGALORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787	02/2018	1,995.34 -	2,400.00	-	11/2021	20.28
299	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789	02/2018	2,177.80 -	2,450.00	-	-	12.50
300	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814	03/2018	1,029.96 -	1,261.05	-	03/2021	22.44
301	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDER - [N24000829	03/2018	1,016.92 -	1,071.00	-	04/2021	5.32
302	FOUR LANING OF POONDYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830	03/2018	2,065.96 -	2,169.00	-	-	4.99

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(September 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
303	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831	03/2018	1,294.47 -	1,296.00	- -	-	.12
304	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842	03/2018	199.90 -	199.90	- -	-	.00
305	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841	03/2018	795.50 -	799.30	- -	07/2021	.48
306	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843	03/2018	196.05 -	196.05	- -	01/2020	.00
307	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853	03/2018	642.13 -	807.00	- -	12/2020	25.68
<u>National Highways Development Project</u>							
308	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371	10/2013	445.89 -	653.29	03/2017 -	09/2019	46.51
309	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388	11/2013	497.05 -	881.05	05/2017 -	05/2020	77.26
<u>Public Works Dept Of State</u>							
310	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306	11/2010	624.41 -	992.67	03/2011 -	12/2019	58.98
311	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308	08/2010	193.69 -	327.92	10/2010 -	12/2019	69.30
312	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	09/2017 -	12/2019	.12
313	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391	11/2015	889.24 -	904.82	- -	-	1.75
314	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396	11/2010	470.20 -	630.36	02/2011 -	-	34.06
315	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407	10/2015	333.21 -	353.89	11/2015 -	-	6.21
316	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415	08/2010	195.04 -	377.99	10/2010 -	06/2020	93.80
317	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531	01/1991	319.68 -	369.77	- -	-	15.67

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(September 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
318	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140	11/2016	215.16 215.00	215.16	09/2019 -	09/2019	.07
319	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141	03/2016	240.30 240.00	240.30	01/2020 -	01/2020	.13
320	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181	08/2010	186.96 -	305.61	09/2014 -	12/2019	63.46
	Total		61,411.63 -	78,315.06			
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
321	NMDC INTEGRATED STEEL PLANT - [N12000086	01/2010	15,525.00 -	23,140.00	05/2015 -	07/2020	49.05
	Total		15,525.00 -	23,140.00			
	<u>TELECOMMUNICATIONS</u>						
	<u>Department Of Telecommunication</u>						
322	NETWORK FOR SPECTRUM - [N26000101	03/2012	13,334.00 -	24,664.00	07/2015 -	05/2020	84.97
	Total		13,334.00 -	24,664.00			
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
323	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088	02/2014	388.00 -	488.28	05/2017 -	10/2019	25.85
324	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 -	2,000.00	10/2019 -	03/2021	64.04
325	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076	06/2014	157.84 -	169.16	03/2017 -	-	7.17
326	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100	02/2016	496.18 496.00	498.99	06/2017 -	10/2020	.60
327	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126	01/2019	790.79 -	800.00	03/2022 -	03/2022	1.16
	<u>Chennai Metro Rail Ltd</u>						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(September 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
328	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]	02/2009	14,600.00 -	19,058.00	12/2015 -	-	30.53
	<u>Hindustan Steelwork Construction Limited</u>						
329	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]	05/2005	768.88 1,070.97	1,113.34	02/2014 -	-	3.96
330	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	03/2007	149.73 173.00	175.94	12/2015 -	-	1.70
	<u>Kochi Metro Rail Corporation Ltd</u>						
331	KOCHI METRO RAIL PROJECT - [N28000081]	07/2012	5,181.79 -	5,687.79	07/2017 -	12/2019	9.77
	<u>National Building Construction Corporation Ltd</u>						
332	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	06/2012	4,264.00 -	4,439.23	11/2019 -	11/2019	4.11
	Total		28,016.42 -	34,430.73			
	<u>WATER RESOURCES</u>						
	<u>Polavaram Project Authority</u>						
333	POLAVARAM IRRIGATION PROJECT - [N30000002]	02/2009	10,151.04 -	55,548.87	03/2020 -	06/2021	447.22
	Total		10,151.04 -	55,548.87			
	Grand Total		4,34,181.54	6,96,459.63			

List of Delayed Projects w.r.t. Latest Schedule

Annexure-XIV

Costing Rs. 150 Crore and above

(September 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
	<u>Bhavini Limited</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 -	6,840.00	5,821.38	09/2010 -	10/2021	133	-
	<u>Nuclear Power Corporation Of India Limited</u>								
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 16,580.00	16,580.00	14,137.00	12/2015 -	06/2020	54	-
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 17,079.00	17,079.00	11,387.00	12/2016 -	12/2020	48	-
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL,TAMIL NADU	03/2013	39,849.00 -	39,849.00	15,706.00	11/2020 -	11/2023	36	-
	Total		67,120.00 -	80,348.00	47,051.38				
	<u>CIVIL AVIATION</u>								
	<u>Airport Authority Of India Limited</u>								
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI,TRIPURA	09/2015	338.93 -	339.00	213.50	06/2019 -	12/2019	6	-
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,A & N ISLANDS	10/2013	314.61 -	441.33	85.79	09/2018 -	06/2020	21	-
7	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPORT - [N04000076]AAI,DELHI	11/2016	233.38 -	233.38	84.73	04/2020 -	12/2020	8	-
8	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA - [N04000080]AAI,WEST BENGAL	01/2016	219.91 -	219.91	61.61	03/2020 -	12/2020	9	-
9	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI - [N04000074]AAI,TAMIL NADU	06/2018	2,467.00 -	2,467.00	213.17	02/2022 -	08/2022	6	-
	Total		3,573.83 -	3,700.62	658.80				
	<u>COAL</u>								
	<u>Bharat Coking Coal Limited</u>								
10	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	269.82	180.83	04/2014 -	11/2019	67	-
11	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	289.45	257.56	05/2014 -	03/2020	70	-
	<u>Central Coal Fields Limited</u>								
12	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	106.41	03/2011 -	03/2021	120	-
13	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	181.17	03/2012 -	03/2021	108	-

Costing Rs. 150 Crore and above

(September 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
14	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	362.49	03/2016 -	03/2021	60	-
15	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	90.78	03/2014 -	03/2021	84	-
16	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	706.40 -	706.40	354.93	07/2012 -	03/2022	116	-
	<u>Eastern Coal Fields Limited</u>								
17	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05 -	1,055.05	510.31	03/2018 -	10/2020	31	-
	<u>Mahanadi Coal Fields Limited</u>								
18	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	302.96	03/2010 -	03/2020	120	-
19	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.10 -	490.10	501.82	03/2017 -	03/2020	36	-
20	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA	05/2014	337.66 -	337.66	183.98	03/2019 -	03/2020	12	-
21	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA	06/2014	289.03 -	289.03	75.85	03/2018 -	03/2020	24	-
22	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	228.90	03/2012 -	03/2021	108	-
23	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	479.53	390.94	03/2013 -	03/2021	96	-
24	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	539.59	03/2013 -	03/2022	108	-
25	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	347.15	03/2010 -	03/2022	144	-
26	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA	05/2014	479.15 -	479.15	200.65	03/2019 -	03/2022	36	-
	<u>Neyveli Lignite Corporation</u>								
27	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 7,080.41	7,080.41	6,730.63	12/2015 -	12/2019	48	-
	<u>Singareni Colliers Company Limited</u>								
28	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78 -	209.78	154.58	03/2015 -	03/2020	60	-
29	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	135.62	06/2015 -	03/2020	57	-
30	KALYANIKHANI OPENCASST PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	384.32	103.95	07/2016 -	03/2020	44	-
31	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 -	415.37	166.43	03/2016 -	03/2020	48	-
32	KAKATIYAKHANI OPENCASST-2 PROJECT - [N06000129]SCCL,TELANGANA	05/2015	397.09 -	442.42	92.46	03/2019 -	03/2020	12	-
33	KOYAGUDEM OPENCASST PROJECT - [N06000146]SCCL,TELANGANA	10/2015	426.79 -	426.79	.72	03/2018 -	03/2020	24	-
34	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL,TELANGANA	11/2016	272.73 -	272.73	162.62	- 04/2017	03/2020	-	35
35	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	164.04	119.59	03/2015 -	03/2021	72	-
36	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	349.28	8.00	03/2015 -	03/2021	72	-

Costing Rs. 150 Crore and above

(September 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
37	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL, TELANGANA	07/2011	447.06 -	473.22	18.35	03/2015 -	03/2021	72	-
38	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]SCCL, TELANGANA	03/2017	413.84 -	413.84	54.51	03/2019 -	03/2022	36	-
39	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL, TELANGANA	12/2009	418.97 -	489.62	343.10	03/2012 -	03/2023	132	-
40	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL, TELANGANA	10/2006	249.03 -	448.86	286.19	03/2012 -	03/2024	144	-
	<u>South-Eastern Coal Fields Limited</u>								
41	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL, CHHATISGARH	09/2008	152.43 -	459.49	193.40	03/2015 -	03/2020	60	-
42	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH	07/2008	178.44 -	178.44	2.88	03/2014 -	03/2020	72	-
43	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL, CHHATISGARH	04/2012	258.56 -	258.56	180.07	03/2016 -	03/2020	48	-
44	AMERA OC RCE - [N06000123]SECL, CHHATISGARH	02/2015	335.97 -	335.97	51.25	03/2018 -	03/2020	24	-
45	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH	12/2009	321.50 -	321.50	192.55	03/2014 -	03/2021	84	-
	<u>Western Coal Fields Limited</u>								
46	ADASA UG TO OC - [N06000133]WCL, MAHARASHTRA	08/2015	288.90 -	333.43	21.02	03/2023 -	03/2024	12	-
47	KAMPTEE DEEP OC MINE - [N06000141]WCL, MAHARASHTRA	11/2015	277.65 -	313.34	116.34	03/2021 -	03/2024	36	-
	Total		18,811.47 -	20,774.20	13,950.58				
	<u>FERTILISERS</u>								
	<u>Rashtriya Chemical & Fertiliser Limited</u>								
48	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF, MAHARASHTRA	10/2014	197.79 -	209.44	174.52	11/2016 -	09/2019	34	-
	Total		197.79 -	209.44	174.52				
	<u>INFORMATION AND BROADCASTING</u>								
	<u>Central Public Works Department</u>								
49	FILM AND TELEVISION INSTITUTE ARUNACHAL PRADESH - [N09000002]CPWD, ANDHRA PRADESH	11/2016	204.32 -	204.32	-	02/2019 -	11/2019	9	-
	Total		204.32 -	204.32	.00				
	<u>PETROLEUM</u>								
	<u>Bharat Petroleum Corporation Limited</u>								
50	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL, TAMIL NADU	11/2012	678.00 -	678.00	5.57	02/2017 -	10/2021	56	-
	<u>Gas Authority Of India Limited</u>								
51	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL, GUJARAT	04/2016	327.78 -	200.00	146.50	04/2018 -	10/2019	18	-

Costing Rs. 150 Crore and above

(September 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
52	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL, MULTI STATE	06/2009	2,915.00 2,915.00	3,049.47	2,524.91	12/2012 -	02/2022	110	-
	<u>Hindustan Petroleum Corporation Limited</u>								
53	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]HPCL, MAHARASHTRA	06/2017	249.26 -	249.26	60.45	06/2020 -	09/2021	15	-
54	120 TMTA NEW LPG PLANT AT BARHI JHARKHAND STATE - [N16000316]HPCL, JHARKHAND	06/2017	161.50 -	161.50	17.78	06/2020 -	09/2021	15	-
	<u>Indian Oil Corporation Limited</u>								
55	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR), CACHAR, ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL, ASSAM	06/2016	423.00 -	423.00	263.70	08/2019 -	09/2019	1	-
56	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]IOCL, ODISHA	05/2016	429.00 -	429.00	311.78	01/2019 -	12/2019	11	-
57	BS-VI PROJECT AT PANIPAT REFINERY - [N16000325]IOCL, HARYANA	12/2017	3,529.00 -	3,529.00	1,720.28	07/2019 -	12/2019	5	-
58	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]IOCL, UTTAR PRADESH	01/2018	666.64 -	666.64	431.71	09/2019 -	01/2020	4	-
59	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY - [N16000322]IOCL, WEST BENGAL	05/2018	2,934.40 -	2,934.40	1,653.76	09/2019 -	01/2020	4	-
60	BS-VI PROJECT AT BONGAIGAON REFINERY - [N16000320]IOCL, ASSAM	05/2018	1,222.00 -	1,222.00	563.53	09/2019 -	02/2020	5	-
61	BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]IOCL, GUJARAT	03/2018	3,380.00 -	3,380.00	2,102.63	09/2019 -	03/2020	6	-
62	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS, HSD AND - [N16000304]IOCL, MADHYA PRADESH	08/2017	236.00 -	236.00	24.15	06/2020 -	08/2020	2	-
63	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL, MULTI STATE	01/2015	690.00 -	690.00	299.12	07/2018 -	10/2020	27	-
64	SITARGANJ LPG PROJECT - [N16000282]IOCL, UTTARAKHAND	02/2017	160.10 -	160.10	41.22	02/2020 -	10/2020	8	-
65	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL, GUJARAT	10/2017	906.00 -	906.00	93.08	02/2020 -	10/2020	8	-
66	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL, TAMIL NADU	05/2016	4,497.00 6,025.00	6,025.00	499.65	12/2018 -	02/2021	26	-
67	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL, WEST BENGAL	04/2017	163.02 -	163.02	50.84	04/2020 -	03/2021	11	-
68	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL, MAHARASHTRA	05/2016	212.00 -	212.00	38.55	01/2021 -	04/2021	3	-
69	LPG BP PROJECT KHORDHA - [N16000283]IOCL, ODISHA	12/2016	161.59 -	161.59	38.29	12/2019 -	07/2021	19	-

Costing Rs. 150 Crore and above

(September 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
70	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH	08/2018	466.00 -	466.00	84.34	04/2021 -	07/2021	3	-
71	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	466.43	30.95	10/2020 -	08/2021	10	-
72	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 -	348.00	30.75	01/2021 -	10/2021	9	-
73	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	318.80	40.06	08/2021 -	11/2021	3	-
74	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	355.00	14.07	04/2022 -	02/2023	10	-
	<u>Mangalore Refinery And Petrochemicals Limited</u>								
75	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA	11/2017	581.00 -	621.00	84.47	03/2020 -	09/2020	6	-
	<u>Oil & Natural Gas Corporation Limited</u>								
76	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 345.92	345.92	146.58	01/2014 -	11/2019	70	-
77	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]ONGC,MAHARASHTRA	02/2019	3,660.71 3,740.05	3,740.05	126.66	04/2021 -	05/2021	1	-
78	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH	03/2016	34,012.00 -	34,012.00	3,411.92	06/2020 -	08/2021	14	-
79	HEERA REDEVELOPMENT - PHASE III - [N16000360]ONGC,MAHARASHTRA	05/2019	2,494.68 -	2,494.68	-	12/2021 -	03/2022	3	-
	<u>Oil India Limited</u>								
80	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM	07/2011	350.00 -	350.00	2.06	01/2019 -	09/2019	8	-
81	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	438.84	230.43	03/2017 -	12/2019	33	-
82	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM	01/2018	543.91 -	682.90	8.97	02/2020 -	06/2020	4	-
	Total		68,093.32 -	70,115.60	15,098.76				
	<u>POWER</u>								
	<u>National Hydro-Electric Power Corporation</u>								
83	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	9,997.11	7,642.51	09/2009 -	12/2021	147	-
	<u>National Thermal Power Corporation</u>								
84	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC,ODISHA	05/2016	1,885.13 -	1,885.13	527.90	12/2018 -	03/2020	15	-

Costing Rs. 150 Crore and above

(September 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
85	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC, WEST BENGAL	12/2016	529.68 -	529.68	140.10	11/2018 -	03/2020	16	-
86	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC, UTTAR PRADESH	09/2014	9,188.98 -	9,188.98	6,502.04	07/2019 03/2020	07/2020	12	4
87	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC, ODISHA	02/2014	12,532.44 -	13,740.53	9,726.03	12/2018 02/2020	09/2020	21	7
88	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC, BIHAR	01/2007	5,353.00 -	9,996.59	7,918.78	07/2012 -	09/2020	98	-
89	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC, UTTARAKHAND	11/2006	2,978.48 5,867.38	5,867.38	4,182.37	03/2013 12/2020	01/2021	94	1
90	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC, JHARKHAND	02/2014	14,366.58 -	15,164.05	9,221.99	06/2019 09/2019	09/2021	27	24
	<u>Power Grid Corporation Of India Limited</u>								
91	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL, RAJASTHAN	07/2016	1,429.38 -	1,429.38	1,045.19	01/2019 07/2019	09/2019	8	2
92	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL, MULTI STATE	10/2011	487.49 -	639.46	564.32	06/2014 -	10/2019	64	-
93	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL, MULTI STATE	01/2015	203.28 -	260.03	193.57	07/2017 -	10/2019	27	-
94	EASTERN REGION STRENGTHENING SCHEME- V - [N18000155]PGCIL, MULTI STATE	10/2013	1,364.52 -	1,891.41	1,263.11	04/2016 -	11/2019	43	-
95	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL, MULTI STATE	01/2015	871.62 -	871.62	582.02	10/2017 -	11/2019	25	-
96	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL, ODISHA	04/2016	844.64 -	844.64	435.06	04/2019 -	11/2019	7	-
97	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL, MULTI STATE	09/2016	562.25 -	562.25	414.25	03/2019 -	11/2019	8	-
98	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL, MULTI STATE	10/2016	608.24 -	608.24	413.61	04/2019 -	11/2019	7	-
99	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL, MULTI STATE	12/2015	3,654.00 -	3,654.00	3,427.57	04/2019 -	11/2019	7	-
100	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL, MULTI STATE	10/2008	4,824.12 -	5,071.94	4,565.74	10/2012 -	12/2019	86	-
101	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL, MULTI STATE	01/2014	374.63 -	374.63	213.02	04/2016 -	12/2019	44	-
102	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL, MULTI STATE	06/2014	5,151.37 -	5,151.37	3,153.93	03/2018 -	12/2019	21	-
103	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL, MULTI STATE	03/2015	197.40 -	197.40	83.07	03/2018 -	12/2019	21	-

Costing Rs. 150 Crore and above

(September 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
104	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	1,394.52	427.71	05/2017 -	12/2019	31	-
105	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE	05/2016	3,519.59 -	3,519.59	2,502.91	05/2019 -	12/2019	7	-
106	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE	10/2016	408.46 -	408.46	288.56	01/2019 -	12/2019	11	-
107	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE	02/2017	322.30 -	322.30	158.10	02/2019 -	12/2019	10	-
108	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE	03/2017	337.75 -	337.75	92.75	06/2019 -	12/2019	6	-
109	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT	05/2017	175.64 -	175.64	100.00	09/2018 -	12/2019	15	-
110	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 -	186.17	107.75	07/2019 -	12/2019	5	-
111	SUPPLEMENTARY TRANS. SYSTEM FOR UMSP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT	12/2017	193.14 -	193.14	97.26	06/2019 -	12/2019	6	-
112	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL	04/2016	454.11 -	454.11	291.64	04/2018 -	01/2020	21	-
113	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE	09/2017	198.49 -	198.49	83.31	09/2019 -	02/2020	5	-
114	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 -	546.36	466.42	11/2016 -	03/2020	40	-
115	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	808.63	525.58	01/2018 -	03/2020	26	-
116	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	235.53	124.27	06/2019 -	03/2020	9	-
117	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA	05/2017	445.89 -	445.89	285.22	02/2019 -	03/2020	13	-
118	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	9,072.36	1,301.58	12/2018 -	12/2020	24	-
119	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	6,880.36	1,641.35	12/2018 -	12/2020	24	-
120	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	14,719.10	12,814.08	08/2013 -	03/2022	103	-

Costing Rs. 150 Crore and above

(September 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>Thdc India Limited</u>								
121	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 -	294.60	310.08	02/2014 -	12/2019	70	-
122	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 -	5,024.35	3,047.08	02/2016 -	06/2022	76	-
123	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	4,397.80	1,770.91	06/2013 -	12/2022	114	-
	Total		1,05,869.27 -	1,37,540.97	88,652.74				
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>HII Infra Tech Services Limited</u>								
124	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	785.00	244.66	04/2020 -	06/2020	2	-
125	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	703.00	184.93	06/2020 -	08/2020	2	-
126	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 -	875.00	39.27	05/2021 -	10/2021	5	-
	<u>Hospital Services Consultancy Corporation</u>								
127	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	272.19	140.58	03/2019 -	10/2019	7	-
	<u>Hospital Services Consultancy Corporation Ltd</u>								
128	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	204.44	188.00	05/2017 -	09/2019	28	-
129	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	152.95	118.23	02/2018 -	09/2019	19	-
130	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	363.99	166.19	05/2018 -	09/2019	16	-
131	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASHTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	274.19	169.93	03/2019 -	10/2019	7	-
132	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL	08/2017	355.15 -	355.15	148.84	03/2019 -	03/2020	12	-
133	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	513.89	147.00	11/2013 -	10/2020	83	-
	Total		4,400.02 -	4,499.80	1,547.63				
	<u>RAILWAYS</u>								
	<u>Central Railways</u>								
134	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50 -	3,712.50	2,380.30	03/2021 -	03/2022	12	-
135	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89 -	1,377.48	308.67	03/2021 -	03/2022	12	-
136	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19 -	1,272.19	296.03	03/2022 -	03/2023	12	-

Costing Rs. 150 Crore and above

(September 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
137	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02 -	540.02	235.70	03/2022 -	03/2024	24	-
138	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 -	1,035.16	90.49	03/2022 -	03/2024	24	-
139	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 -	637.95	58.36	03/2023 -	03/2024	12	-
	<u>Container Corporation Of India</u>								
140	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00 -	305.00	261.28	03/2019 -	12/2019	9	-
141	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	343.00	222.83	03/2019 -	12/2019	9	-
142	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	174.00	151.24	03/2019 -	02/2020	11	-
143	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	493.17	439.80	03/2018 -	03/2020	24	-
144	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32 -	346.32	286.78	03/2019 -	03/2020	12	-
145	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	235.00	11.11	03/2019 -	12/2020	21	-
	<u>East Central Railways</u>								
146	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	528.57	107.81	03/2019 -	12/2019	9	-
147	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	324.73 898.53	1,050.00	1,040.00	03/2012 -	03/2020	96	-
148	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	477.88 751.55	751.55	673.69	03/2012 -	03/2020	96	-
149	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	678.54 678.54	678.54	492.44	03/2019 -	02/2021	23	-
150	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	517.46	03/2020 -	03/2021	12	-
151	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR	12/2015	1,200.20 1,200.20	1,200.20	397.14	03/2020 -	10/2021	19	-
152	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	548.00 -	819.01	489.11	03/2020 -	03/2022	24	-
153	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 1,215.54	1,215.54	63.74	03/2021 -	03/2022	12	-
154	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 1,185.73	1,185.73	32.31	03/2021 -	03/2022	12	-
155	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR	12/2015	1,491.47 -	1,491.47	438.38	03/2020 -	12/2022	33	-
	<u>East Coast Railway</u>								
156	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	238.03	226.50	03/2020 -	03/2021	12	-
157	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 -	1,539.28	924.93	02/2019 -	03/2022	37	-
158	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	810.02	122.59	11/2018 -	03/2022	40	-
159	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	1,160.00 -	1,160.83	682.29	03/2020 -	03/2023	36	-

Costing Rs. 150 Crore and above

(September 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
160	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 -	1,547.38	346.97	03/2022 -	03/2023	12	-
161	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 -	3,791.66	1,237.04	03/2009 -	06/2024	183	-
162	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	1,928.07	691.04	06/2021 -	06/2024	36	-
163	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 -	2,361.74	162.82	03/2022 -	03/2025	36	-
	<u>Eastern Railways</u>								
164	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	157.94	51.75	11/2018 -	03/2021	28	-
165	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	542.18 -	693.80	443.81	03/2020 -	03/2021	12	-
166	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	1,425.44	637.42	02/2013 -	03/2024	133	-
167	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	1,619.48	868.58	03/2019 12/2009	03/2025	72	183
168	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	1,106.62 -	1,091.59	839.63	12/2010 12/2017	03/2025	171	87
169	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	545.70	148.43	03/2006 -	03/2025	228	-
170	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	2,137.81	294.91	03/2022 -	03/2025	36	-
171	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	995.10	448.78	03/2016 -	03/2025	108	-
172	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.51 -	769.40	102.47	03/2017 -	03/2025	96	-
173	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	266.32	160.40	03/2016 -	03/2025	108	-
174	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	296.43	234.43	03/2017 -	03/2025	96	-
175	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	494.59	32.00	03/2005 -	03/2025	240	-
176	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHNACHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96 -	680.68	158.60	02/2012 -	03/2025	157	-
177	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	257.42	106.51	03/2014 -	03/2025	132	-
178	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	108	-

Costing Rs. 150 Crore and above

(September 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>Indian Railway Construction Company Limited</u>								
179	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON, CHHATISGARH	04/2013	3,055.00 -	3,055.00	1,729.64	09/2018 -	12/2020	27	-
180	GEVRA ROAD PENDRA ROAD - [N22000488]IRCON, CHHATISGARH	02/2014	2,288.00 -	4,970.11	619.50	03/2022 -	12/2022	9	-
181	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON, ODISHA	04/2016	5,200.00 -	1,700.43	48.00	03/2020 -	06/2023	39	-
	<u>Metropolitan Rapid Transport Projects</u>								
182	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP) - [220100164]MRTP, MAHARASHTRA	03/1996	495.44 1,781.98	2,980.41	1,417.63	03/2004 -	03/2021	204	-
183	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	63	-
	<u>North Central Railway</u>								
184	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR, MULTI STATE	04/2011	2,912.96 -	3,845.60	137.90	03/2022 -	12/2024	33	-
	<u>North East Frontier Railway</u>								
185	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR - [220100135]NFR, WEST BENGAL	04/1983	297.32 -	614.00	274.97	03/2019 -	03/2020	12	-
186	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR	04/2003	4,454.17 13,809.00	12,524.00	9,123.93	03/2011 -	03/2020	108	-
187	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	385.20 1,532.00	1,532.00	629.19	03/2019 -	03/2020	12	-
188	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR, BIHAR	09/2006	532.87 2,145.00	2,145.00	932.80	03/2019 -	03/2020	12	-
189	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR, ASSAM	04/2011	314.00 728.00	728.00	704.09	03/2019 -	03/2020	12	-
190	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	1,180.19 3,300.00	4,541.00	3,279.71	12/2008 -	03/2021	147	-
191	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND	04/2006	2,326.52 -	4,600.00	781.71	03/2015 -	10/2021	79	-
192	AGARTALA-AKHAURA NL - [N22000195]NFR, TRIPURA	04/2012	569.63 -	650.00	45.24	03/2020 -	12/2021	21	-
	<u>North Eastern Railway</u>								
193	CHHAPRA-BALLIA UP - [N22000134]NER, MULTI STATE	03/2013	295.00 -	477.31	328.19	01/2019 -	01/2020	12	-
194	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER, UTTAR PRADESH	04/2017	622.50 427.00	426.74	179.51	04/2017 -	01/2020	33	-
195	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER, UTTAR PRADESH	04/2016	213.00 -	213.35	8.97	04/2016 -	06/2020	50	-
196	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER, UTTAR PRADESH	04/2016	1,177.96 -	1,028.95	26.06	12/2019 -	04/2021	16	-

Costing Rs. 150 Crore and above

(September 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
197	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	276.90	-	04/2017 -	04/2022	60	-
198	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	150.00	-	04/2017 -	10/2022	66	-
	<u>North Western Railway</u>								
199	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	294.90	141.40	10/2018 -	10/2019	12	-
200	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	303.56	262.32	11/2019 -	05/2020	6	-
201	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 281.03	410.00	351.23	02/2019 -	05/2020	15	-
202	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	348.55	215.47	12/2019 -	06/2020	6	-
203	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	420.18 -	420.18	160.53	03/2020 -	06/2020	3	-
204	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 780.98	886.41	525.78	02/2019 -	03/2021	25	-
205	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	685.99	47.07	03/2020 -	04/2022	25	-
206	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	808.85	47.07	08/2022 -	09/2022	1	-
	<u>Northern Railway</u>								
207	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	694.00	220.42	12/2011 -	03/2021	111	-
208	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 -	845.58	834.59	03/2016 -	03/2021	60	-
209	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	27,949.00	19,403.28	11/2002 -	06/2022	235	-
210	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	2,010.00	654.07	07/2012 -	03/2024	140	-
	<u>Rail Vikas Nigam Ltd.</u>								
211	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	385.00	386.30	03/2009 03/2009	12/2019	129	129
212	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	1,185.64 -	1,844.47	1,783.59	12/2017 -	03/2020	27	-
213	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	1,200.00	1,147.34	03/2019 -	03/2020	12	-
214	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	1,402.02 -	1,100.00	1,050.36	03/2020 -	06/2020	3	-
215	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	816.55	686.11	03/2016 -	12/2020	57	-
216	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	948.04 -	1,500.00	1,323.18	03/2020 -	03/2021	12	-
217	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH	04/2011	1,485.85 -	1,485.85	1,074.88	12/2020 -	03/2021	3	-
218	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70 -	1,202.70	914.39	02/2015 -	12/2021	82	-
219	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,548.66 -	1,548.66	1,268.31	12/2021 -	03/2022	3	-

Costing Rs. 150 Crore and above

(September 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
220	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	1,563.45	03/2020 -	03/2022	24	-
221	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	1,120.00	1,010.21	03/2019 -	06/2022	39	-
222	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	1,183.25	1,072.44	12/2020 -	12/2022	24	-
223	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA	04/2010	2,127.00 -	2,900.00	1,660.87	03/2023 -	03/2024	12	-
224	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60 -	750.56	372.23	03/2022 -	12/2024	33	-
225	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92 -	1,765.92	601.87	03/2023 -	12/2024	21	-
226	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	4,259.48	2,237.39	03/2016 -	03/2025	108	-
227	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	2,913.50	849.88	03/2016 -	03/2025	108	-
228	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00 -	16,216.00	1,655.10	12/2024 -	03/2025	3	-
229	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	2,733.86	40.13	03/2014 -	12/2025	141	-
<u>South Central Railway</u>									
230	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 1.00	1,723.00	1,368.46	03/2000 -	03/2021	252	-
231	KOTLPALI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 -	2,120.16	412.87	03/2009 -	03/2023	168	-
232	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	1,160.48 -	1,160.48	288.38	03/2010 -	03/2023	156	-
233	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	2,063.03	675.97	03/2021 -	03/2023	24	-
234	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	3,631.00	407.42	03/2022 -	03/2023	12	-
235	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 -	2,200.00	252.81	03/2023 -	03/2024	12	-
236	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	2,288.70 -	2,288.70	667.03	03/2021 -	03/2024	36	-
237	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,132.77 -	2,132.77	331.17	03/2014 -	03/2024	120	-
<u>South East Central Railway</u>									
238	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH	04/2010	585.93 737.72	1,300.44	646.30	02/2019 03/2020	06/2020	16	3
<u>South Eastern Railway</u>									

Costing Rs. 150 Crore and above

(September 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
239	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	377.00	180.95	12/2016 08/2018	12/2019	36	16
240	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 358.68	358.68	258.09	12/2018 12/2018	06/2020	18	18
241	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 1,312.96	1,312.96	549.97	03/2020 -	06/2020	3	-
242	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	1,993.24	384.82	03/2021 -	12/2021	9	-
	<u>South Western Railway</u>								
243	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 -	889.52	438.39	03/2017 -	03/2020	36	-
244	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,156.94 -	1,140.93	786.13	03/2020 -	03/2021	12	-
245	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 -	1,870.41	914.00	03/2019 -	03/2021	24	-
246	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	986.30 -	986.30	297.70	03/2016 -	12/2023	93	-
247	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 -	279.54	28.51	03/2016 -	12/2023	93	-
248	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 -	1,382.78	7.35	03/2002 -	03/2024	264	-
249	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	832.47	.94	03/2016 -	03/2024	96	-
250	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 -	2,841.84	113.63	12/2018 -	12/2024	72	-
	<u>Southern Railway</u>								
251	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	1,800.00	170.47	03/2019 -	12/2019	9	-
252	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	2,072.50	1,386.59	02/2019 -	02/2020	12	-
253	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU	10/2013	187.26 -	231.67	108.34	04/2014 -	03/2020	71	-
254	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	980.00	669.21	03/2020 -	03/2021	12	-
255	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU	02/2015	760.00 -	1,182.31	406.32	03/2020 -	06/2021	15	-
256	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	1,567.00	-	03/2024 -	03/2026	24	-
	<u>West Central Railway</u>								
257	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH	12/2015	1,763.93 -	1,763.93	624.49	03/2020 -	03/2022	24	-
258	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH	08/2016	582.13 -	1,247.64	154.63	03/2022 -	09/2022	6	-
259	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	6,093.31	1,835.18	05/2008 -	03/2023	178	-
260	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	424.60 -	2,909.99	1,926.25	03/2021 -	03/2023	24	-

Costing Rs. 150 Crore and above

(September 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
261	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH	06/2016	2,478.23 -	2,478.23	367.59	03/2022 -	03/2023	12	-
	Total		1,57,478.80 -	2,39,305.07	1,04,298.67				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways</u>								
262	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	164.54	89.14	08/2015 -	09/2019	49	-
263	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]MORTH,UTTAR PRADESH	10/2013	445.89 653.00	653.29	464.05	03/2017 -	09/2019	30	-
264	CHIKALI TO KHAMGAON - [N24001012]MORTH,MAHARASHTRA	02/2017	548.03 548.00	548.03	287.00	06/2019 -	10/2019	4	-
265	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA	08/2013	171.96 172.00	172.00	88.30	06/2016 -	11/2019	41	-
266	SAKOLI TO BHANDARA - [N24001118]MORTH,MAHARASHTRA	01/2017	362.96 362.96	362.96	37.83	06/2019 -	11/2019	5	-
267	NASHIK TO PETH - [N24001121]MORTH,MAHARASHTRA	12/2015	289.60 -	289.60	118.81	11/2018 -	11/2019	12	-
268	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA	03/2014	191.50 192.00	192.00	136.19	05/2016 -	12/2019	43	-
269	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MORTH,UTTARAKHAND	06/2017	282.08 -	282.08	77.05	06/2019 -	12/2019	6	-
270	KHAMGAON TO SHEGAON - [N24001009]MORTH,MAHARASHTRA	02/2017	203.21 203.00	203.21	102.79	05/2019 -	12/2019	7	-
271	SHEGAON TO DEORI PHATA - [N24001010]MORTH,MAHARASHTRA	02/2017	373.10 373.00	373.10	123.43	05/2019 -	12/2019	7	-
272	NANDGAON TO MORSHI - [N24001014]MORTH,MAHARASHTRA	01/2017	385.87 386.00	385.87	203.75	06/2019 -	12/2019	6	-
273	MORSHI TO ACHALPUR - [N24001015]MORTH,MAHARASHTRA	01/2017	341.16 341.00	341.16	153.29	06/2019 -	12/2019	6	-
274	NAGAJ TO VAJJAPUR - [N24001023]MORTH,MAHARASHTRA	01/2017	376.72 377.00	376.72	168.81	06/2019 -	12/2019	6	-
275	INDAPUR TO AGARDANDA - [N24001025]MORTH,MAHARASHTRA	01/2017	355.17 355.17	355.17	164.87	07/2019 -	12/2019	5	-
276	TAKARKHED TO JALNA - [N24001085]MORTH,MAHARASHTRA	09/2017	417.90 418.00	417.90	87.26	06/2019 -	12/2019	6	-
277	NAIGAONBANDI TO MANGRULPIR - [N24001094]MORTH,MAHARASHTRA	12/2017	244.04 244.00	244.04	25.94	03/2019 -	12/2019	9	-
278	TALEGAON TO GONAPUR - [N24001096]MORTH,MAHARASHTRA	01/2018	264.41 264.00	264.41	32.71	03/2019 -	12/2019	9	-
279	PEN TO KHOPOLI - [N24001106]MORTH,MAHARASHTRA	03/2018	301.39 302.00	301.39	-	03/2018 -	12/2019	21	-

Costing Rs. 150 Crore and above

(September 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
280	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MORTH,UTTARAKHAND	08/2016	234.88 -	208.89	118.26	12/2017 -	12/2019	24	-
281	AKKALKOT TO DHUDHNI - [N24001120]MORTH,MAHARASHTRA	04/2016	211.42 -	211.42	131.85	02/2019 -	02/2020	12	-
282	INDAPUR TO VADPALE - [N24001114]MORTH,MAHARASHTRA	01/2017	1,202.52 1,202.52	1,202.52	635.90	12/2019 -	03/2020	3	-
283	VADPALE TO BHOGAN KHURD - [N24001115]MORTH,MAHARASHTRA	01/2017	1,598.47 1,598.47	1,598.47	751.91	11/2019 -	03/2020	4	-
284	KOLHA TO NASRATPUR - [N24001111]MORTH,MAHARASHTRA	04/2016	281.78 282.00	281.78	47.73	04/2019 -	04/2020	12	-
285	WAKAN PALI KHOPOLI - [N24001026]MORTH,MAHARASHTRA	01/2017	376.19 376.19	376.19	29.03	05/2019 -	05/2020	12	-
286	DEORI TO AMGAON - [N24001032]MORTH,MAHARASHTRA	01/2017	409.62 410.00	409.62	171.78	05/2019 -	05/2020	12	-
287	DIGRAS DARWAH KARANJA - [N24001013]MORTH,MAHARASHTRA	01/2017	391.06 391.00	391.06	68.00	06/2019 -	06/2020	12	-
288	KARAD TO TAGAON - [N24001053]MORTH,MAHARASHTRA	01/2017	537.81 538.00	537.81	85.97	06/2019 -	06/2020	12	-
289	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MORTH,MAHARASHTRA	02/2017	407.19 407.00	407.19	25.00	06/2019 -	06/2020	12	-
290	MALEWADA TO CHIMUR - [N24001104]MORTH,MAHARASHTRA	10/2016	322.55 -	322.55	156.91	06/2019 -	06/2020	12	-
291	PARLI PIMPLA DAHIGUDA - [N24001138]MORTH,MAHARASHTRA	02/2017	205.72 205.72	205.72	30.42	06/2019 -	06/2020	12	-
292	MANGAON TO DIGHI PORT - [N24001024]MORTH,MAHARASHTRA	01/2017	457.52 457.52	457.52	202.98	07/2019 -	07/2020	12	-
293	WADI TO ASOLA - [N24001022]MORTH,MAHARASHTRA	01/2017	363.82 363.82	363.82	41.10	09/2019 -	09/2020	12	-
294	BARASGAON TO RAHATEE - [N24001113]MORTH,MAHARASHTRA	07/2016	289.11 290.00	289.11	148.00	09/2018 -	04/2021	31	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
295	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH	04/2016	198.00 -	198.00	155.94	10/2016 -	10/2019	36	-
296	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8 - [N24001184]NHIDCL,DELHI	07/2017	269.69 -	269.69	-	09/2019 -	12/2019	3	-
297	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH	12/2016	138.93 155.00	155.00	72.97	01/2017 -	01/2020	36	-
298	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH	03/2015	394.00 -	394.00	272.92	06/2018 -	03/2020	21	-
299	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 339.55	396.52	234.03	08/2016 -	06/2020	46	-

Costing Rs. 150 Crore and above

(September 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
300	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM	05/2015	454.89 -	454.89	123.20	05/2018 05/2020	12/2020	31	7
301	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH	02/2017	168.32 168.32	168.32	33.51	04/2017 02/2018	02/2021	46	36
302	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 180.57	180.57	13.73	04/2017 02/2018	02/2021	46	36
303	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH	02/2017	216.71 216.71	216.71	16.40	04/2017 02/2018	02/2021	46	36
304	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH	02/2017	167.28 167.28	167.28	18.94	04/2017 02/2018	02/2021	46	36
305	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D - [N24000974]NHIDCL,ARUNACHAL PRADESH	02/2017	199.02 199.02	199.02	9.81	- 02/2018	02/2021	-	36
306	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D - [N24000975]NHIDCL,ARUNACHAL PRADESH	02/2017	184.88 184.88	184.88	6.19	- 02/2018	02/2021	-	36
307	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH	03/2017	284.09 284.09	284.09	76.20	04/2017 03/2018	03/2021	47	36
308	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM	01/2016	294.17 -	294.17	63.00	01/2016 02/2019	04/2021	63	26
309	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL,MANIPUR	08/2017	517.57 -	457.77	137.04	10/2018 -	10/2021	36	-
310	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM	06/2015	437.39 -	437.39	9.30	06/2018 12/2020	12/2021	42	12
311	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM	06/2015	463.49 -	463.49	22.32	06/2018 01/2021	12/2021	42	11
312	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH	01/2017	1,253.10 -	1,253.10	158.90	03/2017 -	03/2022	60	-
313	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH	02/2017	175.06 175.06	175.06	12.06	- 04/2019	04/2022	-	36

Costing Rs. 150 Crore and above

(September 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
314	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL,ARUNACHAL PRADESH	02/2017	176.12 176.12	176.12	11.82	- 04/2019	04/2022	-	36
	<u>National Highways Authority Of India</u>								
315	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 1,544.00	1,544.00	1,446.45	09/2016 -	09/2019	36	-
316	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 507.70	507.70	495.63	06/2016 -	09/2019	39	-
317	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 1,240.03	1,057.60	1,000.89	06/2019 12/2016	09/2019	3	33
318	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	637.18	588.00	06/2019 -	09/2019	3	-
319	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	649.00	296.30	06/2019 -	09/2019	3	-
320	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 767.03	767.03	555.72	08/2018 -	09/2019	13	-
321	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	328.47	06/2008 -	10/2019	136	-
322	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	3,220.15	05/2014 -	10/2019	65	-
323	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	425.19	276.40	09/2016 09/2014	10/2019	37	61
324	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 537.16	537.16	500.61	07/2018 -	10/2019	15	-
325	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	972.50	1,492.00	07/2017 -	10/2019	27	-
326	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	479.20	711.38	05/2018 03/2018	10/2019	17	19
327	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	399.54	195.59	04/2019 -	10/2019	6	-
328	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	275.90	257.52	- 02/2016	10/2019	-	44
329	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN	08/2016	320.30 -	320.30	237.81	01/2019 -	10/2019	9	-
330	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN	06/2016	763.23 -	763.23	216.17	06/2019 -	11/2019	5	-
331	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 881.00	688.70	701.76	- 05/2017	11/2019	-	30

Costing Rs. 150 Crore and above

(September 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
332	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH	06/2017	648.33 -	306.00	151.65	06/2017 -	11/2019	29	-
333	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	232.49	-	10/2017 -	11/2019	25	-
334	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	946.00	818.53	06/2018 -	12/2019	18	-
335	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	943.17	08/2012 -	12/2019	88	-
336	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	2,387.46	03/2013 -	12/2019	81	-
337	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,159.10	03/2014 -	12/2019	69	-
338	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	1,364.18	03/2013 -	12/2019	81	-
339	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,173.80	08/2013 -	12/2019	76	-
340	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	1,396.18	2,894.94	09/2014 -	12/2019	63	-
341	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	530.07	556.02	08/2016 -	12/2019	40	-
342	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 -	1,083.00	26.64	06/2018 -	12/2019	18	-
343	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 897.03	897.03	737.19	11/2018 07/2019	12/2019	13	5
344	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 67.34	1,871.34	3,495.79	01/2018 12/2018	12/2019	23	12
345	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI,WEST BENGAL	03/2016	229.37 -	229.37	78.31	11/2018 -	12/2019	13	-
346	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	458.03	303.12	- 12/2017	12/2019	-	24
347	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	248.97	240.44	05/2019 -	12/2019	7	-
348	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	244.90	243.33	05/2019 -	12/2019	7	-
349	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	244.27	141.45	09/2017 -	12/2019	27	-
350	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	597.00	587.64	10/2017 04/2018	01/2020	27	21
351	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	323.72	252.99	08/2018 -	01/2020	17	-

Costing Rs. 150 Crore and above

(September 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
352	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	639.97	274.24	10/2017 -	01/2020	27	-
353	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	478.00	315.11	10/2013 -	02/2020	76	-
354	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	722.46	722.46	07/2018 12/2019	02/2020	19	2
355	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	230.00	337.76	04/2008 -	03/2020	143	-
356	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	470.01	05/2010 -	03/2020	118	-
357	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 2,967.50	2,967.50	3,986.72	11/2011 -	03/2020	100	-
358	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 1,302.98	934.46	531.34	03/2018 -	03/2020	24	-
359	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	1,388.00	1,153.07	08/2018 -	03/2020	19	-
360	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	707.82	343.21	08/2018 -	03/2020	19	-
361	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 3,207.63	1,087.00	473.11	- 02/2018	03/2020	-	25
362	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 2,257.49	667.00	464.05	07/2018 -	04/2020	21	-
363	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 3,007.86	667.00	549.07	06/2018 -	04/2020	22	-
364	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	322.09	77.53	04/2018 -	04/2020	24	-
365	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	804.97	438.27	06/2018 -	04/2020	22	-
366	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	756.27	159.58	03/2020 -	04/2020	1	-
367	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	414.00	531.36	05/2018 03/2019	05/2020	24	14
368	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	923.04	755.97	11/2016 -	05/2020	42	-
369	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	641.17	354.03	07/2018 -	05/2020	22	-

Costing Rs. 150 Crore and above

(September 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
370	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 911.07	904.16	817.58	02/2020 11/2017	05/2020	3	30
371	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	1,065.51	1,027.16	03/2020 -	05/2020	2	-
372	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 2,602.09	1,989.00	852.57	03/2020 11/2017	05/2020	2	30
373	SIX LANNING OF RANASTALAM- ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	1,187.10	778.87	03/2020 -	05/2020	2	-
374	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	641.17	354.03	07/2016 -	05/2020	46	-
375	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,333.68	12/2013 -	06/2020	78	-
376	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,775.04	08/2013 -	06/2020	82	-
377	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	733.33	07/2014 -	06/2020	71	-
378	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 2,182.03	815.28	520.89	06/2018 -	06/2020	24	-
379	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 2,433.38	1,027.53	601.13	06/2018 -	06/2020	24	-
380	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O) - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	1,434.00	645.75	03/2020 -	06/2020	3	-
381	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	1,232.76	278.60	09/2017 -	06/2020	33	-
382	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 2,273.00	2,136.97	1,214.48	12/2018 12/2019	07/2020	19	7
383	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	1,177.00	586.20	03/2020 -	07/2020	4	-
384	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	174.34	224.28	03/2008 -	08/2020	149	-
385	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	423.83	12/2009 -	08/2020	128	-
386	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	329.92	06/2013 01/2019	08/2020	86	19
387	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 870.00	870.00	254.96	03/2019 03/2017	08/2020	17	41
388	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	1,310.00	563.15	03/2020 -	08/2020	5	-

Costing Rs. 150 Crore and above

(September 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
389	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	1,043.28	1,094.73	03/2020 -	08/2020	5	-
390	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	1,160.64	1,082.97	03/2020 -	08/2020	5	-
391	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT	06/2017	1,958.88 -	1,958.88	1,116.85	06/2020 -	08/2020	2	-
392	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	1,227.87	225.96	09/2017 -	08/2020	35	-
393	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	2,700.65	07/2015 12/2019	09/2020	62	9
394	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	2,880.38	06/2014 09/2017	09/2020	75	36
395	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	727.00	421.65	05/2018 -	09/2020	28	-
396	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	504.00	220.70	05/2018 04/2019	09/2020	28	17
397	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	1,176.37	155.12	08/2017 -	09/2020	37	-
398	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	701.40	29.48	03/2019 -	11/2020	20	-
399	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	870.00	36.30	03/2019 -	11/2020	20	-
400	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	1,373.28	571.96	03/2020 -	11/2020	8	-
401	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 1,071.00	1,071.00	549.63	03/2017 05/2018	11/2020	44	30
402	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	964.17	370.32	10/2017 -	11/2020	37	-
403	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	1,655.01	1,867.51	08/2016 -	12/2020	52	-
404	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	2,168.66	621.26	06/2019 -	12/2020	18	-
405	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 1,008.00	1,108.00	1,354.09	08/2019 -	12/2020	16	-
406	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	990.61	17.41	09/2017 -	01/2021	40	-

Costing Rs. 150 Crore and above

(September 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
407	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	400.25	64.89	03/2019 -	02/2021	23	-
408	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	2,510.04	252.10	08/2019 -	03/2021	19	-
409	4-LANNING OF KODEBAD-DHANTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	446.17	38.97	03/2019 -	03/2021	24	-
410	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	1,420.00	365.00	03/2020 -	03/2021	12	-
411	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 1,073.10	1,005.08	-	- 03/2019	03/2021	-	24
412	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA	01/2018	621.00 565.02	621.00	303.91	- 10/2018	04/2021	-	30
413	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH	03/2018	1,532.62 2,499.00	2,499.00	569.15	03/2021 -	04/2021	1	-
414	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	227.77	-	03/2020 -	05/2021	14	-
415	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	476.56	-	07/2017 11/2020	06/2021	47	7
416	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	686.65	80.87	- 07/2020	06/2021	-	11
417	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	953.09	109.21	- 05/2020	06/2021	-	13
418	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	668.86	109.20	- 05/2020	06/2021	-	13
419	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	686.65	75.79	- 03/2020	06/2021	-	15
420	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64 1,687.00	1,437.64	457.31	- 12/2018	07/2021	-	31

Costing Rs. 150 Crore and above

(September 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
421	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	2,485.93	704.29	06/2020 -	09/2021	15	-
422	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 2,190.00	2,400.00	1,555.77	- 05/2019	11/2021	-	30
423	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 1,684.93	1,117.84	-	- 12/2018	12/2021	-	36
424	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	950.64	102.51	08/2017 -	02/2022	54	-
425	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 1,444.25	972.77	-	- 02/2019	02/2022	-	36
<u>National Highways Development Project</u>									
426	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH	10/2013	445.89 -	653.29	464.05	03/2017 -	09/2019	30	-
427	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	410.72 -	410.72	216.14	04/2015 -	10/2019	54	-
428	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH	11/2013	497.05 -	881.05	544.84	05/2017 -	05/2020	36	-
<u>Public Works Dept Of State</u>									
429	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA	03/2015	153.21 -	153.21	100.10	01/2017 -	09/2019	32	-
430	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA	12/2011	159.39 -	159.39	210.29	11/2017 -	09/2019	22	-
431	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO - [N24001143]PWD,UTTAR PRADESH	10/2016	176.94 177.00	176.94	132.45	10/2018 -	09/2019	11	-
432	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH - [N24001145]PWD,UTTAR PRADESH	05/2013	164.54 165.00	164.54	89.14	08/2015 -	09/2019	49	-
433	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]PWD,MADHYA PRADESH	11/2017	235.91 -	235.91	117.24	02/2018 -	11/2019	21	-
434	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]PWD,MADHYA PRADESH	11/2017	184.62 -	184.62	55.27	02/2018 -	11/2019	21	-
435	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]PWD,MADHYA PRADESH	03/2018	214.69 -	214.69	23.06	03/2018 -	11/2019	20	-

Costing Rs. 150 Crore and above

(September 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
436	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]PWD,MADHYA PRADESH	03/2018	233.04 -	233.04	95.28	03/2018 -	11/2019	20	-
437	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]PWD,MADHYA PRADESH	11/2017	254.17 -	254.17	139.86	02/2018 -	11/2019	21	-
438	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 - [N24000895]PWD,MADHYA PRADESH	09/2016	287.34 -	287.34	148.65	01/2019 -	11/2019	10	-
439	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]PWD,MADHYA PRADESH	03/2016	877.79 -	877.79	436.12	06/2019 -	11/2019	5	-
440	REHABILITATION AND UPGRADATION OF TULSI PUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]PWD,UTTAR PRADESH	03/2016	249.50 -	249.50	150.70	05/2019 -	11/2019	6	-
441	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]PWD,MADHYA PRADESH	11/2017	392.33 -	392.33	242.88	03/2018 -	11/2019	20	-
442	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA	01/2014	255.75 348.00	348.43	290.12	09/2017 -	12/2019	27	-
443	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	992.67	853.82	03/2011 -	12/2019	105	-
444	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	327.92	254.24	10/2010 -	12/2019	110	-
445	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 240.58	151.59	196.76	08/2013 -	12/2019	76	-
446	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 269.14	269.14	185.49	02/2013 09/2017	12/2019	82	27
447	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	191.08	99.98	08/2015 -	12/2019	52	-
448	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]PWD,MADHYA PRADESH	03/2018	162.56 -	162.56	88.47	03/2018 -	12/2019	21	-
449	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]PWD,TELANGANA	10/2016	298.32 -	298.32	77.44	02/2019 -	12/2019	10	-
450	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]PWD,TELANGANA	10/2016	248.83 -	248.83	88.85	03/2019 -	12/2019	9	-

Costing Rs. 150 Crore and above

(September 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
451	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]PWD,TELANGANA	01/2017	300.00 -	300.00	99.46	05/2019 -	12/2019	7	-
452	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997]PWD,TELANGANA	03/2018	192.67 -	192.67	107.37	07/2019 -	12/2019	5	-
453	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM - [N24001153]PWD,ASSAM	11/2010	197.37 -	197.37	88.86	02/2014 -	12/2019	70	-
454	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]PWD,MIZORAM	08/2010	186.96 -	305.61	275.06	09/2014 -	12/2019	63	-
455	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]PWD,MADHYA PRADESH	11/2017	249.05 -	249.05	118.29	07/2018 -	01/2020	18	-
456	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH	03/2015	511.83 -	511.83	240.05	08/2017 -	02/2020	30	-
457	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]PWD,MADHYA PRADESH	01/2016	809.16 -	809.16	219.42	07/2018 -	02/2020	19	-
458	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	954.43 -	954.43	235.61	09/2015 -	03/2020	54	-
459	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]PWD,MADHYA PRADESH	02/2018	279.44 -	279.44	76.00	03/2018 -	04/2020	25	-
460	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]PWD,MADHYA PRADESH	01/2017	373.82 -	373.82	116.34	09/2019 -	05/2020	8	-
461	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]PWD,KARNATAKA	05/2018	171.60 -	171.60	.86	05/2018 -	05/2020	24	-
462	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	377.99	305.38	10/2010 -	06/2020	116	-
463	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]PWD,MADHYA PRADESH	03/2018	166.21 -	166.21	30.52	08/2018 -	06/2020	22	-
464	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]PWD,MADHYA PRADESH	01/2017	205.05 -	205.05	73.22	03/2017 -	06/2020	39	-
465	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]PWD,MADHYA PRADESH	03/2018	217.22 -	217.22	20.43	08/2018 -	06/2020	22	-
466	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]PWD,MADHYA PRADESH	02/2018	169.63 -	169.63	9.35	03/2018 -	07/2020	28	-
467	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]PWD,BIHAR	05/2014	199.98 -	199.98	153.43	08/2016 -	12/2020	52	-

Costing Rs. 150 Crore and above

(September 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
468	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION - [N24001173]PWD,KARNATAKA	02/2017	157.32 188.00	157.32	-	05/2019 -	05/2021	24	-
469	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]PWD,WEST BENGAL	03/2016	160.27 213.97	213.97	20.11	08/2019 -	08/2021	24	-
470	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]PWD,WEST BENGAL	06/2016	236.78 263.26	263.26	59.92	08/2019 -	08/2021	24	-
	Total		1,35,969.46 -	1,41,677.21	90,440.14				
	<u>TELECOMMUNICATIONS</u>								
	<u>Department Of Telecommunication</u>								
471	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	24,664.00	8,397.00	07/2015 -	05/2020	58	-
	Total		13,334.00 -	24,664.00	8,397.00				
	<u>URBAN DEVELOPMENT</u>								
	<u>Ahmedabad Metro Rail</u>								
472	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT	11/2014	10,773.00 -	10,773.00	6,057.03	12/2018 -	07/2020	19	-
	<u>Bangalore Metro Rail Corporation Limited</u>								
473	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	26,405.14	499.85	02/2019 -	03/2020	13	-
	<u>Central Public Works Department</u>								
474	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	156.13	08/2016 -	10/2019	38	-
475	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	199.91	11/2014 -	10/2019	59	-
476	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB	02/2014	388.00 -	488.28	437.01	05/2017 -	10/2019	29	-
477	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	266.00	-	12/2013 -	10/2019	70	-
478	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]CPWD,PUNJAB	08/2016	294.00 -	294.00	203.32	04/2019 -	02/2020	10	-
479	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN	12/2016	549.31 559.47	559.47	348.69	07/2019 12/2019	02/2020	7	2
480	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	165.23	92.05	10/2012 -	03/2020	89	-

Costing Rs. 150 Crore and above

(September 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
481	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD,TAMIL NADU	12/2015	209.00 -	209.00	130.62	10/2019 -	03/2020	5	-
482	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	85.33	03/2016 -	09/2020	54	-
483	RESIDENTIAL QUATERS FOR HAL,BANGLORE - [N28000103]CPWD,KARNATAKA	12/2016	246.31 -	246.31	72.38	02/2020 -	09/2020	7	-
484	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR	02/2014	216.69 -	216.69	52.00	03/2015 -	10/2020	67	-
485	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	498.99	92.22	06/2017 -	10/2020	40	-
486	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI	06/2015	197.33 -	197.33	48.86	04/2019 -	11/2020	19	-
487	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB - [N28000120]CPWD,PUNJAB	01/2018	430.00 -	430.00	77.69	05/2020 -	01/2021	8	-
488	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	2,000.00	374.71	10/2019 -	03/2021	17	-
489	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 -	392.00	12.56	- 08/2020	03/2021	-	7
490	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA	10/2016	209.84 -	209.84	35.79	03/2020 -	05/2021	14	-
	<u>Hindustan Steelwork Construction Limited</u>								
491	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72	-
	<u>Kochi Metro Rail Corporation Ltd</u>								
492	KOCHI METRO RAIL PROJECT - [N28000081]KMRL,KERALA	07/2012	5,181.79 -	5,687.79	5,188.00	07/2017 -	12/2019	29	-
	<u>Mumbai Metro Rail Corporation Ltd</u>								
493	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	05/2020	64	-
	<u>Nagpur Metro Rail Corporation Ltd</u>								
494	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	8,680.00	6,237.34	03/2018 -	12/2019	21	-
	Total		80,858.55 -	82,410.33	21,052.70				
	<u>WATER RESOURCES</u>								
	<u>Polavaram Project Authority</u>								
495	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA,ANDHRA PRADESH	02/2009	10,151.04 -	55,548.87	16,417.99	03/2020 -	06/2021	15	-

Costing Rs. 150 Crore and above

(September 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	Total		10,151.04 -	55,548.87	16,417.99				
	Grand Total		6,66,061.87	8,60,998.43	4,07,740.91				

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2019)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12/2020	12320	48
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	06/2020	11459	54
3	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	NPCIL	03/2013	11/2020	11/2023	39849	36
4	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2021	3492	133

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	AAI	09/2015	06/2019	12/2019	338.93	6
6	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	AAI	01/2016	03/2020	12/2020	219.91	9
7	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	AAI	06/2018	02/2022	08/2022	2467	6
8	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2020	314.61	21
9	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	AAI	11/2016	04/2020	12/2020	233.38	8

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
10	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1	SCCL	03/2017	03/2019	03/2022	413.84	36
11	RFR OF MANUGURU OC PROJECT	SCCL	11/2012	03/2016	03/2020	430.45	48
12	KALYANIKHANI OPENCAST PROJECT	SCCL	07/2012	07/2016	03/2020	417.33	44
13	RG OC -III EXTENSION (PHASE -II) PROJECT	SCCL	06/2012	06/2015	03/2020	365.01	57
14	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2021	162.76	72
15	KANIHA OCP, MCL, (10.0 MTY)	MCL	12/2007	03/2013	03/2022	457.77	108
16	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2009	03/2014	03/2021	321.5	84
17	BHUBANESWARI OCP, MCL (20.0 MTY)	MCL	12/2007	03/2017	03/2020	490.1	36
18	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	03/2012	03/2021	207.28	108
19	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2021	479.53	96
20	RKP OCP PHASE-I	SCCL	03/2010	03/2015	03/2020	209.78	60

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
21	BALRAM OCP EXTENSION, MCL 8.00 MTY	MCL	12/2007	03/2010	03/2022	172.08	144
22	NEYVELI NEW THERMAL POWER PROJECT (2X500 MW)	NLC	06/2011	12/2015	12/2019	5907.11	48
23	JALAGAM VENGALA RAO OCP-II	SCCL	07/2011	03/2015	03/2021	447.06	72
24	MAGADH OC 20 MTY (CCL)	CCL	08/2008	07/2012	03/2022	706.4	116
25	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2023	418.97	132
26	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2021	163.51	120
27	TAPIN OCP (2.5 MTY)	CCL	08/2008	03/2012	03/2021	264.68	108
28	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2021	162.46	84
29	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2024	249.03	144
30	KISTARAM OCP	SCCL	11/2010	03/2015	03/2021	242.29	72
31	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2020	178.44	72
32	KULDA EXPN OC. (5.00 MTY)	MCL	06/2014	03/2018	03/2020	289.03	24
33	AMERA OC RCE	SECL	02/2015	03/2018	03/2020	335.97	24
34	MADHUBAND NLW WASHERY	BCCL	08/2010	05/2014	03/2020	289.45	70
35	PATHERDIH NLW WASHERY	BCCL	10/2012	04/2014	11/2019	269.82	67
36	KAKATIYAKHANI OPENCAST-2 PROJECT	SCCL	05/2015	03/2019	03/2020	397.09	12
37	ADASA UG TO OC	WCL	08/2015	03/2023	03/2024	288.9	12
38	KULDA OCP (MAHANADI COALFIELDS LTD)	MCL	01/2005	03/2010	03/2020	302.96	120
39	RAJRAPPA RCE OCP (3.0 MTY)	CCL	12/2009	03/2016	03/2021	510.85	60
40	BAROUD OC EXPANSION (RCE)- 3MTY	SECL	04/2012	03/2016	03/2020	258.56	48
41	KOYAGUDEM OPENCAST PROJECT	SCCL	10/2015	03/2018	03/2020	426.79	24
42	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	60
43	KAMPTEE DEEP OC MINE	WCL	11/2015	03/2021	03/2024	277.65	36

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
44	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	ECL	08/2012	03/2018	10/2020	1055.05	31
45	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	MCL	05/2014	03/2019	03/2022	479.15	36
46	JAGANNATH RE-ORGANISATION OC.(6.00 MTY)	MCL	05/2014	03/2019	03/2020	337.66	12

FERTILISERS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
47	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	RCF	10/2014	11/2016	09/2019	197.79	34

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
48	NEIGRIHMS SHILLONG MEGHALYA	HSCC	10/2016	05/2018	09/2019	363.99	16
49	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH	HSCC	08/2017	03/2019	10/2019	272.19	7
50	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA	HSCC	08/2017	03/2019	10/2019	274.19	7
51	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	HSCC	08/2017	03/2019	03/2020	355.15	12
52	LHMC NEW DELHI-RE-DEVELOPMENT	HSCC	02/2013	11/2013	10/2020	414.11	83
53	AIIMS - MOTHER AND CHILD BLOCK	HSCC	12/2013	05/2017	09/2019	204.44	28
54	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	HSCC	07/2016	02/2018	09/2019	152.95	19

INFORMATION AND BROADCASTING

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
55	FILM AND TELEVISION INSTITUTE ARUNACHAL PRADESH	CPWD	11/2016	02/2019	11/2019	204.32	9

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
56	REVAMPING OF FACILITIES AT VIZAG TERMINAL	IOCL	04/2018	04/2022	02/2023	355	10
57	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	02/2022	1112	32
58	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	IOCL	12/2017	10/2020	08/2021	466.43	10
59	PARADIP LPG IMPORT FACILITY	IOCL	01/2015	07/2018	10/2020	690	27

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
60	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III	ONGC	11/2014	04/2019	12/2019	6068.8	8
61	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY	ONGC	08/2015	03/2019	05/2020	2818.88	14
62	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	11/2019	202.94	70
63	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	12/2019	861.79	79
64	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	IOCL	05/2016	01/2021	10/2021	348	9
65	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY	IOCL	05/2016	01/2019	12/2019	429	11
66	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG	ONGC	04/2017	09/2018	09/2019	420.76	12
67	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)	ONGC	02/2017	05/2021	12/2021	4006.83	7
68	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	OIL	07/2011	01/2019	09/2019	350	8
69	KHARAGPUR LPG BOTTLING PLANT	IOCL	04/2017	04/2020	03/2021	163.02	11
70	BS-VI PROJECT AT GUJARAT REFINERY	IOCL	03/2018	09/2019	03/2020	3380	6
71	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE	IOCL	10/2017	02/2020	10/2020	906	8
72	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	OIL	07/2011	03/2017	12/2019	352.56	33
73	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	12/2019	2059.63	57
74	HALDIA LPG IMPORT FACILITY	BPCL	03/2015	10/2018	12/2019	694	14
75	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	11/2019	4588.29	15
76	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	GAIL	04/2016	04/2018	10/2019	327.78	18
77	IRUGUR-DEVANGONTHI POL PIPELINE	BPCL	11/2012	02/2017	10/2021	678	56
78	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	ONGC	11/2015	03/2019	05/2020	650.82	14
79	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	ONGC	03/2016	06/2020	08/2021	34012	14
80	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	02/2021	4497	26
81	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA	ONGC	01/2015	12/2017	03/2020	4619.94	27

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
82	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	05/2020	3190.69	25
83	SITARGANJ LPG PROJECT	IOCL	02/2017	02/2020	10/2020	160.1	8
84	LPG BP PROJECT KHORDHA	IOCL	12/2016	12/2019	07/2021	161.59	19
85	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	02/2022	2915	110
86	SEA WATER DESALINATION PLANT	MANGALORE REFI	11/2017	03/2020	09/2020	581	6
87	ASSAM RENEWAL PROJECT FOR GROUP A	ONGC	03/2009	03/2013	12/2019	2465.15	81
88	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE	MANGALORE REFI	10/2015	03/2019	10/2019	135	7
89	BSVI UPGRADATION	MANGALORE REFI	09/2016	12/2019	07/2020	1810	7
90	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY	BPCL	02/2016	02/2020	10/2020	3313	8
91	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE	HPCL	06/2017	06/2020	09/2021	161.5	15
92	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA	HPCL	06/2017	06/2020	09/2021	249.26	15

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
93	DURGAPUR PP-III (2X20 MW) - NSPCL	NTPC	12/2016	11/2018	03/2020	529.68	16
94	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	12/2020	4754.42	24
95	EASTERN REGION STRENGTHENING SCHEME XVII(PART B)	PGCIL	02/2017	06/2019	03/2020	235.53	9
96	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	12/2019	4824.12	86
97	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	01/2018	03/2020	11638.55	26
98	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	03/2022	11130.19	103
99	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	11/2019	1364.52	43
100	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	PGCIL	01/2014	04/2016	12/2019	374.63	44
101	EASTERN REGION STRENGTHENING SCHEME-XII	PGCIL	05/2014	11/2016	03/2020	522.29	40
102	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	01/2021	2978.48	94
103	TRANSMISSION SYSTEM STRENGTHENING IN	PGCIL	06/2014	03/2018	12/2019	5151.37	21

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH						
104	TANDA TPP STAGE-II (2X660 MW)	NTPC	09/2014	07/2019	07/2020	9188.98	12
105	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	12/2018	09/2020	12532.44	21
106	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	09/2021	14366.58	27
107	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	02/2022	1381.84	29
108	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP)	PGCIL	01/2015	10/2017	11/2019	871.62	25
109	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII	PGCIL	01/2015	07/2017	10/2019	203.28	27
110	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	PGCIL	03/2015	03/2018	12/2019	197.4	21
111	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	PGCIL	03/2015	05/2017	12/2019	1394.52	31
112	DHUKWAN SMALL HYDRO PROJECT	THDCIL	05/2011	02/2014	12/2019	195.42	70
113	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	07/2012	09/2020	5353	98
114	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2022	2491.58	114
115	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	10/2019	2496.9	118
116	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	06/2022	1657	76
117	SYTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	10/2019	487.49	64
118	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	08/2021	8692.97	118
119	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	10/2017	03/2020	11846	29
120	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	NTPC	01/2016	11/2020	06/2021	10598.98	7
121	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	PGCIL	03/2016	01/2018	03/2020	808.63	26
122	EASTERN REGION STRENGTHENING SCHEME- XV	PGCIL	04/2016	04/2018	01/2020	454.11	21
123	GREEN ENERGY CORRIDORS - INTER STATE TRANSSMISSION SCHEME PART-D	PGCIL	05/2016	05/2019	12/2019	3519.59	7
124	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA	PGCIL	04/2016	04/2019	11/2019	844.64	7
125	TRAMMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN	PGCIL	07/2016	01/2019	09/2019	1429.38	8

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
126	SOUTHERN REGION STRENGTHENING SCHEME-XXI	PGCIL	09/2016	03/2019	11/2019	562.25	8
127	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	PGCIL	12/2015	04/2019	11/2019	3654	7
128	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT	PGCIL	05/2017	09/2018	12/2019	175.64	15
129	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B)	PGCIL	05/2017	02/2019	03/2020	445.89	13
130	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	03/2021	12964.6	34
131	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	02/2017	06/2020	9750.89	40
132	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2021	3919.59	147
133	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	PGCIL	10/2016	04/2019	11/2019	608.24	7
134	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II)	PGCIL	10/2016	01/2019	12/2019	408.46	11
135	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/	PGCIL	02/2017	02/2019	12/2019	322.3	10
136	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII	PGCIL	03/2017	06/2019	12/2019	337.75	6
137	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	12/2020	5111.33	24
138	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL	NTPC	05/2016	12/2018	03/2020	1885.13	15
139	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPF AT BANASKANTHA (RADHANESDA) GUJARAT	PGCIL	12/2017	06/2019	12/2019	193.14	6

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
140	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM	WR	04/2017	03/2020	03/2021	691.84	12
141	RAMNA - SINGRAULI DOUBLING	ECR	08/2015	03/2020	03/2021	2436.21	12
142	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL	IRCON	04/2016	03/2020	06/2023	5200	39
143	KARAILA ROAD - SHAKTINAGAR DOUBLING	ECR	08/2015	03/2019	12/2019	528.57	9
144	MULTI MODAL LOGISTICS PARK AT KATHUWAS	CCOI	01/2011	03/2018	03/2020	493.17	24
145	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN	CCOI	10/2013	03/2019	12/2019	305	9
146	MULTI MODAL LOGISTICS PARK AT BARHI	CCOI	12/2015	03/2019	03/2020	346.32	12
147	MULTI MODAL LOGISTICS PARK AT TIHI	CCOI	12/2015	03/2019	02/2020	174	11

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
148	MULTI MODAL LOGISTICS PARK AT VARNAMA	CCOI	10/2013	03/2019	12/2019	343	9
149	INDARA - DOHRIGHAT GAUGE CONVERSION.	NER	04/2016	04/2016	06/2020	213	50
150	GUNTUR-GUNTAKAL	SCR	04/2016	03/2022	03/2023	3631	12
151	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM	SR	10/2013	04/2014	03/2020	187.26	71
152	JAGADALPUR-KORAPUT DOUBLING	ECOR	04/2015	03/2022	03/2023	1547.38	12
153	KORAPUT - SINGAPUR ROAD DOUBLING	ECOR	04/2015	03/2022	03/2025	2361.74	36
154	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	03/2022	701.61	40
155	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	ECOR	04/2015	12/2018	03/2022	1172.92	39
156	KAZIPET-BALHRSHA	SCR	04/2015	03/2021	03/2023	2063.03	24
157	BONDAMUNDA RANCHI DOUBLING	SER	03/2016	03/2021	12/2021	1724.2	9
158	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	RVNL	04/2015	03/2022	12/2024	943.6	33
159	NEW BG RLY LINE FROM EKLAKHI- BALURGHAT INCLUDING GAZOLE- ITAHAR(NL), NEFR	NFR	04/1983	03/2019	03/2020	297.32	12
160	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2023	1045.2	168
161	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	03/2025	1188.91	72
162	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	03/2024	607.09	133
163	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	12/2017	03/2020	1185.64	27
164	RAMGANJMUNDI-BHOPAL (NL), WCR	WCR	04/2001	03/2021	03/2023	424.6	24
165	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	12/2021	1202.7	82
166	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	12/2019	133.41	129
167	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	06/2024	810.78	36
168	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI- THIRU 'PONDI'-AGASTIYAMPALLI	SR	09/2007	02/2019	02/2020	724.69	12
169	BARDHAMAN-KATWA (GC)	ER	04/2007	12/2010	03/2025	1106.62	171

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
170	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	03/2022	2393.47	96
171	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	03/2020	477.88	96
172	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	03/2010	03/2023	1160.48	156
173	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	03/2025	2913.51	108
174	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	03/2023	3503.69	12
175	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	ER	04/2010	03/2016	03/2025	277.28	108
176	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL	ER	04/2010	03/2017	03/2025	365.17	96
177	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS)	ER	04/2010	11/2018	03/2021	157.94	28
178	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	03/2022	792.89	12
179	HANSDIHA-GODDA NL	ER	04/2011	03/2020	03/2021	542.18	12
180	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY	ER	04/2011	03/2017	03/2026	299.6	108
181	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL	ER	04/2010	03/2005	03/2025	494.54	240
182	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	02/2012	03/2025	499.96	157
183	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL	ER	04/2009	03/2014	03/2025	257.42	132
184	3RD LINE BETWEEN BHUSAWAL-JALGAON	CR	04/2011	03/2019	12/2019	184.06	9
185	WARDHA-SEWAGRAM NGP 3RD LINE	CR	04/2012	03/2022	03/2024	540.02	24
186	BAGALKOT-KUDACHI NL	SWR	04/2010	03/2016	12/2023	986.3	93
187	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	03/2023	03/2024	1856.95	12
188	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	03/2021	287	111
189	SHIMOGA-HARIHAR NL	SWR	04/2011	03/2016	03/2024	832.47	96
190	NADIKUDE-SRI KALAHASTI	SCR	04/2011	03/2021	03/2024	2288.7	36
191	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	SCR	04/2008	03/2014	03/2024	2132.77	120
192	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	RVNL	04/2010	03/2023	03/2024	2127	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
193	GADAG-WADI NL	SWR	04/2013	12/2018	12/2024	2841.84	72
194	MARIKUPPAM - KUPPAM	SWR	04/2012	03/2016	12/2023	279.54	93
195	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	03/2022	2271.5	12
196	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	03/2021	495.44	204
197	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2023	247.66	178
198	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	03/2020	324.73	96
199	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	03/2021	1180.19	147
200	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	06/2024	2923.13	183
201	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2020	4454.17	108
202	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	03/2020	385.2	12
203	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	03/2020	532.87	12
204	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	10/2021	2326.52	79
205	MUMBAI URBAN TRANSPORT PROJECT PHASE- II	M RTP	04/2008	03/2014	03/2021	5300	84
206	DAUSA-GANGAPUR CITY(NL), NWR	NWR	02/1997	02/2019	03/2021	410.08	25
207	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	03/2024	450	140
208	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	06/2022	2500	235
209	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	03/2025	3951.98	108
210	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	141
211	MUNEERABAD-MAHABOONNAGAR(NL), SCR	SCR	04/1997	03/2000	03/2021	1723	252
212	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	04/2020	12/2020	511.86	8
213	BANGLORE - SATYAMANGALAM (NL)(SWR)	SWR	04/1996	03/2002	03/2024	1382.78	264
214	TIRUCHIRAPPALI-NAGORE- KARAIKKAL(SR)(GC)	SR	09/1995	03/2020	03/2021	303.98	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
215	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	WR	04/2008	03/2012	03/2022	318.24	120
216	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	03/2021	829.74	12
217	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	03/2022	1503.71	24
218	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	03/2022	1111.99	37
219	BHADRAK - NERGUNDI 3RD LINE	ECOR	03/2013	10/2020	03/2023	843.04	29
220	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	03/2020	03/2023	1160	36
221	SAMBALPUR - ANGUL RLY. ELECTRIFICATION	ECOR	03/2012	03/2020	03/2021	155.81	12
222	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	SER	04/2012	12/2016	12/2019	148.77	36
223	HUBLI- CHIKJAJUR	SWR	03/2015	03/2020	03/2021	1156.94	12
224	PHULERA - DIGANA DOUBLING	NWR	05/2015	03/2020	04/2022	600	25
225	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	03/2021	1614.59	24
226	HAJIPUR - BACHAWARA	ECR	05/2015	03/2019	02/2021	678.54	23
227	ALWAR-BANDIKUI DOUBLING	NWR	04/2013	02/2019	05/2020	242.09	15
228	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	12/2018	06/2020	258.2	18
229	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	03/2022	548	24
230	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	12/2021	569.63	21
231	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	03/2019	03/2020	314	12
232	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2020	632.68	57
233	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI	SR	04/2011	03/2019	12/2019	120.7	9
234	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	ER	04/1987	03/2006	03/2025	406.99	228
235	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	03/2025	915.98	36
236	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	01/2020	295	12
237	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	M RTP	03/2013	03/2016	06/2021	4874.58	63

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
238	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	12/2019	06/2020	246.08	6
239	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	WR	04/2007	03/2022	03/2023	1640.04	12
240	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	03/2022	320.66	36
241	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	03/2021	03/2022	1037.15	12
242	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	12/2024	2912.96	33
243	THIYAT HAMIRA-SANU	NWR	04/2013	10/2018	10/2019	236.93	12
244	AJMER-BANGURGRAM	NWR	04/2011	11/2019	05/2020	213.39	6
245	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3	ER	04/2001	03/2016	03/2025	923.52	108
246	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	ER	04/2005	03/2017	03/2025	595.51	96
247	KIUL - GAYA DOUBLING PROJECT	ECR	12/2015	03/2020	10/2021	1200.2	19
248	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	ECR	12/2015	03/2020	12/2022	1491.47	33
249	KATNI - SINGRAULI DOUBLING PROJECT	WCR	12/2015	03/2020	03/2022	1763.93	24
250	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	CR	02/2015	03/2022	03/2023	1272.19	12
251	MANMAD - JALGAON - 3RD LINE (160 KM)	CR	02/2016	03/2022	03/2024	1035.16	24
252	WARDHA - NAGPUR - 4TH LINE (76 KM)	CR	02/2016	03/2023	03/2024	637.95	12
253	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	03/2030	1027.4	324
254	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	03/2020	927.01	12
255	MAU-GHAZIPUR-TARIGHAT NEW LINE	RVNL	04/2015	03/2023	12/2024	1765.92	21
256	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	03/2021	948.04	12
257	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	06/2022	942.95	39
258	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	RVNL	03/2012	12/2020	12/2022	1183.25	24
259	KATNI-BINA 3RD LINE (263 KM)	WCR	06/2016	03/2022	03/2023	2478.23	12
260	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	09/2022	582.13	6

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
261	NANPARA - NEPALGANJ GAUGE CONVERSION.	NER	04/2017	04/2017	10/2022	150	66
262	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION	NER	04/2017	04/2017	01/2020	622.5	33
263	ETAH - KASGANJ - NEW LINE	NER	04/2017	04/2017	04/2022	276.9	60
264	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING.	NER	04/2016	12/2019	04/2021	1177.96	16
265	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	03/2022	744.04	12
266	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	03/2022	731.64	12
267	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	03/2023	229	15
268	JHARSUGUDA-BILASPUR 4TH LINE	SECR	04/2015	03/2021	12/2022	1973	21
269	MULTI MODAL LOGISTICS PARK AT KAKINADA	CCOI	08/2016	03/2019	12/2020	234.5	21
270	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	06/2020	585.93	16
271	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM)	SR	02/2017	03/2024	03/2026	1567	24
272	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	SR	02/2015	03/2020	06/2021	760	15
273	JALANDHAR-PATHANKOT-JAMMU TAWI	NR	03/2002	03/2016	03/2021	625	60
274	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	IRCON	04/2013	09/2018	12/2020	3055	27
275	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	12/2022	2288	9
276	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	03/2020	644.78	36
277	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	WR	02/1991	03/2019	03/2020	551.51	12
278	INDORE-DEWAS-UJJAIN (80 KMS)	WR	04/2016	06/2020	06/2021	700	12

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
279	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	PWD	08/2010	09/2014	12/2019	186.96	63
280	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION	PWD	02/2017	05/2019	05/2021	157.32	24
281	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT	PWD	05/2018	05/2018	05/2020	171.6	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
282	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM	PWD	11/2010	02/2014	12/2019	197.37	70
283	BALANCE WORK FOR REHABILITATION AND UPGRADEMENT OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM.	PWD	11/2017	03/2018	11/2019	392.33	20
284	REHABILITATION AND UPGRADEMENT OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730	PWD	03/2016	05/2019	11/2019	249.5	6
285	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH	PWD	05/2013	08/2015	09/2019	164.54	49
286	REHABILITATION AND UPGRADEMENT OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH	MORTH	10/2013	03/2017	09/2019	445.89	30
287	REHABILITATION AND UPGRADEMENT OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO	PWD	10/2016	10/2018	09/2019	176.94	11
288	PARLI PIMPLA DAHIGUDA	MORTH	02/2017	06/2019	06/2020	205.72	12
289	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST	NHAI	01/2017	05/2019	12/2019	244.9	7
290	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER	MORTH	08/2016	12/2017	12/2019	234.88	24
291	NASHIK TO PETH	MORTH	12/2015	11/2018	11/2019	289.6	12
292	AKKALKOT TO DHUDHNI	MORTH	04/2016	02/2019	02/2020	211.42	12
293	BARASGAON TO RAHATEE	MORTH	07/2016	09/2018	04/2021	289.11	31
294	KOLHA TO NASRATPUR	MORTH	04/2016	04/2019	04/2020	281.78	12
295	PEN TO KHOPOLI	MORTH	03/2018	03/2018	12/2019	301.39	21
296	MALEWADA TO CHIMUR	MORTH	10/2016	06/2019	06/2020	322.55	12
297	TALEGAON TO GONAPUR	MORTH	01/2018	03/2019	12/2019	264.41	9
298	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	PWD	11/2010	03/2011	12/2019	624.41	105
299	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	PWD	08/2010	10/2010	12/2019	193.69	110
300	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	PWD	01/2013	02/2013	12/2019	182.28	82
301	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	PWD	08/2010	10/2010	06/2020	195.04	116
302	FOUR LANNING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	NHAI	03/2016	07/2016	05/2020	641.17	46
303	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	NHAI	08/2017	08/2017	02/2022	950.64	54
304	FOUR LANNING OF CHOLOPURAM-THANJAVUR	NHAI	08/2017	08/2017	09/2020	1176.37	37

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
305	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	NHAI	07/2017	07/2017	06/2021	476.56	47
306	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40)	NHAI	06/2017	06/2017	11/2019	648.33	29
307	JUNAGADH BYPASS	NHAI	10/2017	10/2017	11/2019	232.49	25
308	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124.	NHAI	10/2017	10/2017	01/2020	639.97	27
309	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540	NHAI	10/2017	10/2017	11/2020	964.17	37
310	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	06/2020	1124.11	33
311	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69	NHAI	09/2017	09/2017	01/2021	990.61	40
312	4-LANNING OF OTTANCHATRAM BYPASS	NHAI	09/2017	09/2017	12/2019	244.27	27
313	4-LANNING OF STHIYATHOPU-CHOLOPURAM	NHAI	09/2017	09/2017	08/2020	1227.87	35
314	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES	PWD	03/2015	10/2015	11/2019	271.45	49
315	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	NHIDCL	05/2015	05/2018	12/2020	454.89	31
316	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	NHIDCL	06/2015	06/2018	12/2021	437.39	42
317	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5	NHIDCL	06/2015	06/2018	12/2021	463.49	42
318	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	NHIDCL	03/2015	06/2018	03/2020	394	21
319	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S	NHIDCL	10/2014	03/2018	12/2019	369	21
320	EPC- CORRIDOR APPROACH WORKS - NH (0): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM	PWD	03/2015	01/2017	09/2019	153.21	32
321	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1	PWD	01/2014	09/2017	12/2019	255.75	27
322	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270	NHDP	10/2013	03/2017	09/2019	445.89	30
323	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	NHDP	11/2013	05/2017	05/2020	497.05	36
324	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE	MORTH	05/2013	08/2015	09/2019	164.54	49
325	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200	PWD	03/2015	08/2017	02/2020	511.83	30
326	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA	PWD	12/2011	11/2017	09/2019	159.39	22
327	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA	PWD	12/2011	08/2015	12/2019	191.08	52

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
328	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) 0	NHIDCL	01/2016	01/2016	04/2021	294.17	63
329	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	NHIDCL	01/2016	01/2016	12/2021	252	71
330	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	PWD	11/2011	09/2015	03/2020	954.43	54
331	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP	NHDP	01/2012	04/2015	10/2019	410.72	54
332	GWALIOR-JHANSI, NH-75	NHAI	12/2003	12/2009	08/2020	604	128
333	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	NHAI	07/2010	07/2015	09/2020	1987	62
334	SRINAGAR TO BANIHAL	NHAI	06/2011	06/2014	09/2020	1100.7	75
335	KRISHNANAGAR-BERHAMPUR	NHAI	02/2012	07/2014	06/2020	702.16	71
336	DELHI/ HARYANA BORDER TO ROHTAK	NHAI	04/2007	05/2010	03/2020	486	118
337	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	03/2020	1108	100
338	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM	NHAI	02/2010	08/2012	12/2019	617	88
339	PUNE-SATARA(NH-4)	NHAI	10/2010	03/2013	12/2019	1724.55	81
340	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	09/2019	1266.6	36
341	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	NHAI	09/2011	12/2013	06/2020	1250	78
342	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	12/2019	2848	69
343	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	NHAI	11/2011	05/2014	10/2019	1535	65
344	MUZAFFARNAGAR-HARIDWAR	NHAI	09/2011	03/2013	12/2019	754	81
345	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	08/2013	12/2019	1078.84	76
346	4-LANING OF BRAHAMPUR-FARAKA	NHAI	02/2011	08/2013	06/2020	998.79	82
347	6-LANING OF DHANKUNI-KHARAGPUR SECTION	NHAI	04/2012	09/2014	12/2019	1396.18	63
348	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA	NHAI	11/2012	08/2016	12/2019	530.07	40
349	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	NHAI	01/2015	07/2017	10/2019	972.5	27
350	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION	NHAI	06/2014	11/2016	05/2020	923.04	42

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
351	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	NHAI	05/2014	08/2016	12/2020	1655.01	52
352	FOUR LANING OF HOSPET - CHITRADURGA	NHAI	03/2015	08/2018	03/2020	1388	19
353	FOUR LANING OF AURANGABAD - YEDISHI	NHAI	07/2015	01/2018	12/2019	1871.34	23
354	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	PWD	04/2013	08/2013	12/2019	151.59	76
355	SONAPUR TO GUWAHTI (AS-3)	NHAI	12/2003	03/2008	08/2020	245	149
356	NALBARI T BIJNI (AS-7)	NHAI	12/2003	04/2008	03/2020	208	143
357	NALBARI TO BIJNI (AS-6)	NHAI	12/2003	06/2008	10/2019	225	136
358	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	NHAI	09/2010	06/2018	12/2019	946	18
359	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	NHAI	06/2011	06/2013	08/2020	600	86
360	HARIDWAR DEHRADUN APPROVED LENGTH 69	NHAI	11/2011	10/2013	02/2020	478.51	76
361	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR	NHAI	09/2014	09/2016	10/2019	425.19	37
362	2 LANING WITH PS OF GULABPURA - UNIARA	NHAI	10/2015	10/2017	01/2020	597	27
363	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D	NHAI	09/2015	05/2018	05/2020	414.51	24
364	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	09/2020	531.13	28
365	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	NHAI	10/2015	05/2018	06/2020	593.26	25
366	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	NHAI	12/2015	03/2019	04/2021	649.5	25
367	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	NHAI	12/2015	06/2016	09/2019	602.95	39
368	4 LANING OF AMBALA - KAITHAL - PACKAGE -2	NHAI	01/2016	07/2018	10/2019	574.28	15
369	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3	NHAI	08/2015	05/2018	09/2020	505	28
370	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	NHAI	12/2015	06/2018	12/2019	1083	18
371	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A	NHAI	12/2015	06/2019	12/2020	2168.66	18
372	FOUR LANING OF PARWANOO -SOLAN	NHAI	09/2015	03/2018	03/2020	934.46	24
373	FOUR LANING OF YADGIRI - WARANGAL	NHAI	12/2015	11/2018	12/2019	1423.96	13

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
374	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A	NHAI	12/2015	12/2018	07/2020	2136.97	19
375	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II)	NHAI	01/2016	06/2018	06/2020	815.28	24
376	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I)	NHAI	01/2016	06/2018	06/2020	1027.53	24
377	FOUR LANING OF SIMGA - SARAGAON	NHAI	12/2015	05/2018	10/2019	596.67	17
378	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III)	NHAI	06/2016	07/2018	04/2020	667	21
379	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II)	NHAI	12/2015	06/2018	04/2020	667	22
380	FOUR LANING OF FORBESGANJ - JOGBANI	NHAI	08/2015	04/2018	04/2020	322.09	24
381	FOUR LANING OF CHANDIGARH - KHARAR	NHAI	10/2015	12/2017	12/2019	447.29	24
382	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1)	NHAI	12/2015	04/2018	03/2020	726.67	23
383	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	NHAI	12/2015	05/2018	10/2019	479.2	17
384	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA	NHAI	08/2015	04/2019	10/2019	399.54	6
385	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	NHAI	03/2016	04/2019	10/2019	1587.49	6
386	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	NHAI	03/2016	03/2019	11/2020	701.4	20
387	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA	NHAI	03/2016	11/2018	12/2019	229.37	13
388	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL	NHAI	03/2016	03/2019	11/2020	870	20
389	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH	NHAI	02/2016	08/2018	03/2020	707.82	19
390	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791	NHAI	03/2016	04/2019	07/2020	899	15
391	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K	NHAI	02/2016	07/2018	05/2020	641.17	22
392	NAGPUR RING ROAD PACKAGE-1	NHAI	03/2016	07/2019	12/2020	546	17
393	NAGPUR RING ROAD PACKAGE-2	NHAI	03/2016	07/2019	12/2020	591.66	17
394	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T	NHAI	04/2016	06/2018	04/2020	804.97	22
395	FOUR LANING OF BARHI-HAZARIBAGH NH-33	NHAI	08/2016	08/2018	01/2020	323.72	17
396	HOSPET-BELLARY-KARNATAKA AP BORDER	NHAI	08/2016	03/2019	08/2020	1167.42	17

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
397	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500	NHAI	08/2016	04/2019	11/2019	2016	7
398	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73	NHAI	08/2016	05/2019	12/2019	248.97	7
399	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR	NHAI	08/2016	01/2019	10/2019	320.3	9
400	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM.	NHIDCL	04/2016	10/2016	10/2019	198	36
401	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S	NHAI	09/2016	08/2019	03/2021	2510.04	19
402	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA	NHAI	09/2016	08/2018	09/2019	767.03	13
403	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	NHAI	09/2016	08/2019	12/2020	950.69	16
404	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI	NHAI	11/2016	03/2019	02/2021	400.25	23
405	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT	NHAI	11/2016	03/2019	03/2021	446.17	24
406	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	NHAI	11/2012	07/2018	02/2020	605.84	19
407	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO	MORTH	03/2014	05/2016	12/2019	191.5	43
408	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR	MORTH	08/2013	06/2016	11/2019	171.96	41
409	NAIGAONBANDI TO MANGRULPIR	MORTH	12/2017	03/2019	12/2019	244.04	9
410	TAKARKHED TO JALNA	MORTH	09/2017	06/2019	12/2019	417.9	6
411	KARAD PATAN CHIPLUN GUHAGAR	MORTH	02/2017	06/2019	06/2020	407.19	12
412	KARAD TO TAGAON	MORTH	01/2017	06/2019	06/2020	537.81	12
413	DEORI TO AMGAON	MORTH	01/2017	05/2019	05/2020	409.62	12
414	WAKAN PALI KHOPOLI	MORTH	01/2017	05/2019	05/2020	376.19	12
415	MANGAON TO DIGHI PORT	MORTH	01/2017	07/2019	07/2020	457.52	12
416	NAGAJ TO VAIJAPUR	MORTH	01/2017	06/2019	12/2019	376.72	6
417	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2	NHAI	03/2017	03/2020	11/2020	1373.28	8
418	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580)	NHAI	03/2017	03/2017	11/2020	1059.73	44

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
419	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE	NHAI	03/2017	03/2020	05/2021	235.48	14
420	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	03/2021	1288.07	12
421	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	NHIDCL	12/2016	01/2017	01/2020	138.93	36
422	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	NHIDCL	01/2017	03/2017	03/2022	1253.1	60
423	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	NHIDCL	03/2017	04/2017	03/2021	284.09	47
424	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS	NHIDCL	02/2017	04/2017	02/2021	168.32	46
425	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	NHIDCL	02/2017	04/2017	02/2021	180.57	46
426	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS	NHIDCL	02/2017	04/2017	02/2021	216.71	46
427	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	NHIDCL	02/2017	04/2017	02/2021	167.28	46
428	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	NHIDCL	03/2016	08/2016	06/2020	396.52	46
429	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P	NHAI	06/2017	06/2020	09/2021	2485.93	15
430	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	MORTH	06/2017	06/2019	12/2019	282.08	6
431	WADI TO ASOLA	MORTH	01/2017	09/2019	09/2020	363.82	12
432	MORSHI TO ACHALPUR	MORTH	01/2017	06/2019	12/2019	341.16	6
433	NANDGAON TO MORSHI	MORTH	01/2017	06/2019	12/2019	385.87	6
434	DIGRAS DARWAH KARANJA	MORTH	01/2017	06/2019	06/2020	391.06	12
435	SHEGAON TO DEORI PHATA	MORTH	02/2017	05/2019	12/2019	373.1	7
436	KHAMGAON TO SHEGAON	MORTH	02/2017	05/2019	12/2019	203.21	7
437	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC	PWD	05/2014	08/2016	12/2020	199.98	52
438	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION	PWD	01/2017	05/2019	12/2019	300	7
439	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ	PWD	10/2016	03/2019	12/2019	248.83	9
440	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON	PWD	10/2016	02/2019	12/2019	298.32	10
441	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM	MORTH	01/2017	01/2018	01/2020	576.48	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	KM 128/927 TO KM 195/000 OF NH						
442	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216	MORTH	01/2017	09/2017	09/2019	263.45	24
443	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2	MORTH	11/2016	08/2017	03/2020	376.25	31
444	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT	MORTH	01/2016	08/2016	03/2020	348.95	43
445	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216	MORTH	03/2016	09/2016	03/2020	444.84	42
446	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD	MORTH	08/2016	01/2017	12/2019	350.61	35
447	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P	MORTH	01/2018	08/2018	08/2020	418.03	24
448	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O	MORTH	03/2016	05/2016	03/2020	995.09	46
449	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA	MORTH	03/2018	11/2018	05/2020	504.19	18
450	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (	MORTH	03/2018	07/2018	01/2020	297.12	18
451	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG	MORTH	03/2018	08/2018	02/2020	289.67	18
452	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU	MORTH	03/2018	08/2018	02/2020	244.95	18
453	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3	MORTH	03/2018	08/2018	03/2020	228.32	19
454	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V	MORTH	02/2017	11/2017	11/2019	429.43	24
455	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD	MORTH	01/2017	08/2017	03/2020	319.28	31
456	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69	MORTH	11/2016	05/2017	03/2020	290.15	34
457	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO	MORTH	11/2016	01/2018	01/2020	378.24	24
458	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU	MORTH	09/2016	02/2017	12/2019	372.68	34
459	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12	MORTH	10/2015	12/2015	12/2019	333.21	48
460	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS	PWD	01/2017	03/2019	09/2019	247.25	6
461	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS	PWD	01/2016	07/2018	02/2020	809.16	19
462	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A	PWD	01/2017	09/2019	05/2020	373.82	8
463	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175	PWD	09/2016	01/2019	11/2019	287.34	10

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
464	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS	PWD	02/2018	03/2018	04/2020	279.44	25
465	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS	PWD	11/2017	02/2018	11/2019	254.17	21
466	2L+PS OF THIKRI ANJAD SECTION OF NH-347B	PWD	11/2017	07/2018	01/2020	249.05	18
467	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS	PWD	03/2018	03/2018	11/2019	233.04	20
468	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS	PWD	03/2018	08/2018	06/2020	217.22	22
469	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS	PWD	03/2018	03/2018	11/2019	214.69	20
470	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH.	PWD	01/2017	03/2017	06/2020	205.05	39
471	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N	PWD	06/2016	08/2019	08/2021	236.78	24
472	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND	PWD	03/2016	08/2019	08/2021	160.27	24
473	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS	PWD	11/2017	02/2018	11/2019	184.62	21
474	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID	PWD	11/2017	02/2018	11/2019	235.91	21
475	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA	PWD	02/2018	03/2018	07/2020	169.63	28
476	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H	PWD	03/2016	11/2018	11/2019	271.17	12
477	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS	PWD	03/2018	08/2018	06/2020	166.21	22
478	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS	PWD	03/2018	03/2018	12/2019	162.56	21
479	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	NHIDCL	08/2017	10/2018	10/2021	517.57	36

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
480	CENTRAL DISPATCH YARD	RINL	08/2015	08/2018	10/2019	320.66	14
481	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	SAIL	11/2016	06/2019	06/2020	262.87	12
482	NEW SINTER PLANT AT BOKARO STEEL PLANT	SAIL	03/2015	10/2017	06/2020	1034.01	32
483	INSTALLATION OF NEW HOT STRIP MILL AT RSP	SAIL	04/2015	04/2018	11/2019	3127.3	19
484	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	07/2020	15525	62

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
485	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	SAIL	05/2015	12/2017	11/2019	1154.18	23
486	FORGED WHEEL PLANT	RINL	04/2014	09/2018	10/2019	1682.85	13
487	COKE OVEN BATTERY-5	RINL	12/2011	12/2017	10/2019	2858	22

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
488	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	05/2020	13334	58
489	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	BSNL	01/2018	10/2018	12/2019	231.8	14

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
490	AHMEDABAD METRO RAIL PROJECT PHASE 1	MEGA	11/2014	12/2018	07/2020	10773	19
491	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	CPWD	02/2014	03/2015	10/2020	216.69	67
492	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	CPWD	02/2014	05/2017	10/2019	388	29
493	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	CPWD	02/2014	08/2016	10/2019	156.57	38
494	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	CPWD	11/2012	11/2014	10/2019	270.83	59
495	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	CPWD	09/2012	03/2016	09/2020	171.86	54
496	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	03/2021	1219.21	17
497	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	CPWD	01/2010	10/2012	03/2020	165.23	89
498	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	12/2019	5181.79	29
499	NAGPUR METRO RAIL	NMRCL	08/2014	03/2018	12/2019	8680	21
500	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	01/2015	05/2020	23136	64
501	BANGALORE METRO RAIL PROJECT PHASE-2	BMRCL	02/2014	02/2019	03/2020	26405.14	13
502	IRRIGATION WORK OF BAGMATI	HSCL	10/2005	03/2015	03/2021	956	72
503	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	CPWD	06/2015	04/2019	11/2020	197.33	19
504	RESIDENTIAL QUATERS FOR HAL, BANGLORE	CPWD	12/2016	02/2020	09/2020	246.31	7

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
505	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	CPWD	02/2016	06/2017	10/2020	496.18	40
506	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD	CPWD	10/2016	03/2020	05/2021	209.84	14
507	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	10/2019	114.26	70
508	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	CPWD	08/2016	04/2019	02/2020	294	10
509	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	CPWD	12/2016	07/2019	02/2020	549.31	7
510	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	CPWD	01/2018	05/2020	01/2021	430	8

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
511	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	06/2021	10151.04	15

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(SEPTEMBER 2019)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	6840	3348
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	11459	16580	5121
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12320	17079	4759

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	314.61	441.33	126.72

COAL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
5	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	152.43	459.49	307.06
6	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	5907.11	7080.41	1173.3
7	RANIGANJ MASTER PLAN	ECL	08/2009	08/2019	2661.73	5186.24	2524.51
8	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	162.76	349.28	186.52
9	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	249.03	448.86	199.83
10	BHANEGAON OC	WCL	02/2015	03/2023	187.94	409.68	221.74

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
11	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPR	01/2006	01/2012	993	1693	700
12	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	607.06	714.25	107.19
13	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	202.94	345.92	142.98
14	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	1112	1507.24	395.24
15	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)	ONGC	02/2017	05/2021	4006.83	4475.92	469.09
16	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	2915	3049.47	134.47
17	MUMBAI REFINERY EXPANSION PROJECT	HPCL	09/2015	03/2020	4199	5060	861
18	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	4497	6025	1528

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
19	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	4588.29	5245.96	657.67
20	HALDIA LPG IMPORT FACILITY	BPCL	03/2015	10/2018	694	1097.54	403.54
21	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	871.35	1200	328.65
22	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	2059.63	2665.65	606.02
23	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	OIL	01/2018	02/2020	543.91	682.9	138.99
24	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	861.79	1683.06	821.27
25	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	IOCL	01/2015	12/2020	1823	3027.9	1204.9
26	PARADIP HYDERABAD PIPELINE	IOCL	01/2015	12/2020	2321	3338	1017

POWER

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
27	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	9997.11	6077.52
28	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	01/2018	11638.55	12865.92	1227.37
29	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	11130.19	14719.1	3588.91
30	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	19496.34	13211.01
31	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	4824.12	5071.94	247.82
32	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	5111.33	6880.36	1769.03
33	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	4754.42	9072.36	4317.94
34	PAKRI BARWADIH COAL MINING PROJECT	NTPC	10/2004	10/2017	4237.96	4552	314.04
35	KHARGONE STPP STAGE I (1320 MW)	NTPC	03/2015	01/2020	9870.51	11148.86	1278.35
36	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	2496.9	7927.34	5430.44
37	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	2491.58	4397.8	1906.22
38	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	02/2017	9750.89	12176.28	2425.39
39	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	12964.6	17304	4339.4
40	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	07/2012	5353	9996.59	4643.59

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
41	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	1381.84	1592.34	210.5
42	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	14366.58	15164.05	797.47
43	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	12/2018	12532.44	13740.53	1208.09
44	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	5867.38	2888.9
45	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	NTPC	07/2012	08/2017	1527	1801.07	274.07
46	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	10/2017	11846	12739.82	893.82
47	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	8692.97	21312.11	12619.14
48	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	1779.29	2187.32	408.03
49	SYTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	487.49	639.46	151.97
50	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	1657	5024.35	3367.35
51	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	1364.52	1891.41	526.89
RAILWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
52	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR	NFR	04/1983	03/2019	297.32	614	316.68
53	KODERMA-RANCHI VIA BARKAKANA (NL), ECR	ECR	03/1999	N.A.	1033.07	3376	2342.93
54	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	1045.2	2120.16	1074.96
55	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	M RTP	03/2000	12/2006	1049.69	3404.92	2355.23
56	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	1188.91	1619.48	430.57
57	RAMGANJMUNDI-BHOPAL (NL), WCR	WCR	04/2001	03/2021	424.6	2909.99	2485.39
58	CHHINDWARA - NAGPUR (GC)(SECR)	SECR	04/2005	N.A.	383.79	1413.76	1029.97
59	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	477.88	751.55	273.67
60	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	ECR	04/2003	N.A.	528.65	2066.78	1538.13
61	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	2393.47	5021.45	2627.98

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
62	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	171.1	275.08	103.98
63	TIDIVANAM-NAGARI (NL)	SR	09/2006	N.A.	582.83	2300	1717.17
64	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	SR	09/2006	N.A.	227.4	900	672.6
65	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII' -AGASTIYAMPALLI	SR	09/2007	02/2019	724.69	2072.5	1347.81
66	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	810.78	1928.07	1117.29
67	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	133.41	385	251.59
68	CUMBUM-PRODDATUR	SCR	04/2013	N.A.	829	1599.39	770.39
69	SRINIVASA-PURA-MADANAPALLI NL	SWR	04/2013	N.A.	296	466.65	170.65
70	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	SWR	04/2013	N.A.	558	692.43	134.43
71	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL	NR	04/2007	N.A.	336.91	800	463.09
72	BHANUPALI-BILASPUR BERI NL	RVNL	04/2008	12/2026	2966.99	7000	4033.01
73	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	287	694	407
74	BHADRACHALAM-KOVVUR	SCR	04/2012	N.A.	923.23	1787	863.77
75	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	03/2023	1856.95	2200	343.05
76	MANUGURU-RAMAGUNDAM	SCR	04/2013	N.A.	1112	2911.84	1799.84
77	DAUSA-GANGAPUR CITY(NL),NWR	NWR	02/1997	02/2019	410.08	886.41	476.33
78	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	4084.69	2745.21
79	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	2326.52	4600	2273.48
80	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	532.87	2145	1612.13
81	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	385.2	1532	1146.8
82	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	495.74	734.01	238.27
83	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	4454.17	12524	8069.83
84	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	2923.13	3791.66	868.53

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
85	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	1180.19	4541	3360.81
86	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	2912.96	3845.6	932.64
87	RATLAM-DUNGARPUR VIA BANSWARA (NL)	NWR	04/2011	N.A.	2082.75	4079.15	1996.4
88	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	320.66	858.96	538.3
89	AHMEDABAD-BOTAD (GC)	RVNL	04/2012	12/2021	975.62	1082.32	106.7
90	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	12/2019	246.08	348.55	102.47
91	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	MRTPT	03/2013	03/2016	4874.58	8574.97	3700.39
92	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	295	477.31	182.31
93	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP	NER	03/2007	12/2021	243.78	895	651.22
94	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP	NER	03/2013	N.A.	307	1409.09	1102.09
95	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR	ECR	04/1998	N.A.	180.82	726.31	545.49
96	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	731.64	1185.73	454.09
97	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	744.04	1215.54	471.5
98	BURHWAL - GONDA - 3RD RUNNING LINE.	NER	04/2016	N.A.	602.5	714.34	111.84
99	CHANDIGARH-BADDI	NR	04/2007	03/2023	328.14	1540	1211.86
100	WESTERN DEDICATED FREIGHT CORRIDOR	DFCC	11/2007	03/2020	16592	51101	34509
101	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE	NER	04/2017	01/2018	1343	1476.15	133.15
102	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	SR	02/2015	03/2020	760	1182.31	422.31
103	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	SR	02/1996	03/2005	268.87	950	681.13
104	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	585.93	1300.44	714.51
105	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	1908.51	2686.63	778.12
106	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	582.13	1247.64	665.51

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
107	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	942.95	1120	177.05
108	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	948.04	1500	551.96
109	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	713.48	1950	1236.52
110	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	927.01	1200	272.99
111	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	1027.4	2373	1345.6
112	BONDAMUNDA RANCHI DOUBLING	SER	03/2016	03/2021	1724.2	1993.24	269.04
113	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	969.83	1312.96	343.13
114	DIGARU-HOJAI (102 KM)	NFR	04/2015	03/2021	870.96	2136.01	1265.05
115	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	701.61	810.02	108.41
116	KOTTAVALSA - KORAPUT DOUBLING	ECOR	04/2015	03/2022	2499.71	3382.95	883.24
117	MUZAFFARPUR-SITAMARHI NEW LINE	ECR	01/1991	07/2014	332.15	546.71	214.56
118	VIJAYAWADA-GUDUR	RVNL	04/2015	12/2023	3246.26	3548.67	302.41
119	KONDAPALLI-KOTHAGUDEM	SCR	04/2013	N.A.	723	997.09	274.09
120	DAUND - MANMAD (236 KM)	CR	02/2016	03/2023	1876	2081.27	205.27
121	VAIBHAVWADI -KOLHAPUR (107 KM)	CR	02/2016	03/2024	2750	3438.51	688.51
122	PUNE-NASIK (265 KM)	CR	02/2016	03/2024	2425	5341.68	2916.68
123	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	DFCC	10/2006	N.A.	11589	28181	16592
124	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	ER	04/2005	03/2017	595.51	769.4	173.89
125	PIRPAINTI-BHAGALPUR	ER	04/2011	N.A.	261.38	471.81	210.43
126	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	915.98	2137.81	1221.83
127	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR	ER	04/2007	N.A.	450	1261.34	811.34
128	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	ER	04/1987	03/2006	406.99	545.7	138.71
129	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI	SR	04/2011	03/2019	120.7	1800	1679.3

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
130	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	632.68	816.55	183.87
131	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	03/2019	314	728	414
132	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	NFR	04/1999	N.A.	819.23	1871	1051.77
133	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	03/2020	414.84	661	246.16
134	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	394.28	152.76
135	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	03/2020	242.22	471	228.78
136	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	03/2021	906.46	6000	5093.54
137	MADURAI-BODINAYAKKANUR	SR	04/2008	N.A.	164.41	450	285.59
138	ERODE-PALANI	SR	04/2008	N.A.	288.57	1140	851.43
139	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	NFR	04/2010	N.A.	221.42	380	158.58
140	KURUPPANTHARA-CHINGAVANAM	SR	04/2007	N.A.	270.14	457.08	186.94
141	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	SR	04/1999	N.A.	198.68	556.64	357.96
142	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	SR	04/2013	N.A.	839	1500	661
143	CHENNAI-CUDDALORE VIA MAMALLAPURAM	SR	04/2008	N.A.	523.52	2300	1776.48
144	ATTIPPATTU PUTTUR	SR	04/2008	02/2019	151.84	1105	953.16
145	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	NFR	04/2013	03/2019	1798	2496.67	698.67
146	HAJIPUR-RAMDAYALUNAGAR DOUBLING	ECR	04/2013	N.A.	213.01	425.17	212.16
147	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	548	819.01	271.01
148	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	ECR	04/2004	N.A.	372.14	1470.5	1098.36
149	MOTIHARI-SITAMARHI (NL)	ECR	04/2006	N.A.	211	1006	795
150	CHHAPRA-MUZAFFARPUR (NL)	ECR	04/2006	N.A.	378.56	2609	2230.44
151	SAKRI-HASANPUR ROAD (NL)	ECR	04/1999	N.A.	325	735.2	410.2
152	BIHTA-AURANGABAD (NL)	ECR	04/2008	N.A.	326.2	2995.01	2668.81

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
153	GAYA-CHATRA (NL)	ECR	04/2008	N.A.	415.67	549.75	134.08
154	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	12/2018	258.2	358.68	100.48
155	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	651	1009	358
156	BOWAICHANDI-ARAMBAGH	SER	04/2010	N.A.	267.37	620	352.63
157	ALWAR-BANDIKUI DOUBLING	NWR	04/2013	02/2019	242.09	410	167.91
158	PUSHKAR-MERTA	NWR	04/2013	N.A.	323	432.22	109.22
159	AJMER-KOTA (NASIRABAD-JAUNDRI)	NWR	04/2013	N.A.	822	1099.54	277.54
160	ANGAMALI-SABARIMALA (N.L.)(SR)	SR	10/1998	N.A.	1566	2815.62	1249.62
161	KODERMA-TILAIYA (NL), ECR	ECR	04/2002	N.A.	459.91	1625.87	1165.96
162	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	1614.59	1870.41	255.82
163	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	NWR	05/2015	N.A.	873.71	1980.21	1106.5
164	SAMASTIPUR-DARBANGHA	ECR	05/2015	N.A.	380	519.33	139.33
165	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	SER	04/2012	12/2016	148.77	377	228.23
166	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	1111.99	1539.28	427.29
167	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	829.74	1310.23	480.49
168	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKAWA-JAIN	NFR	02/1999	04/2010	380.6	1871	1490.4
169	JALANDHAR-PATHANKOT-JAMMU TAWI	NR	03/2002	03/2016	625	845.58	220.58
170	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	2288	4970.11	2682.11
171	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	WR	02/1991	03/2019	551.51	809.07	257.56
172	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	644.78	889.52	244.74
173	CHAMPA-JHARSUGUDA 3RD LINE	SECR	04/2008	12/2019	872	1226.51	354.51
174	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	229	860.92	631.92
175	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIIYAWAN-BIHARSHARIF,	ECR	04/1991	N.A.	329.39	1483.14	1153.75

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
176	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	09/1995	03/2020	303.98	980	676.02
177	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	393.46	1026	632.54
178	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	04/2020	511.86	1756.92	1245.06
179	NANDYAL-YERRAGUNTALA(NL), SCR	SCR	03/1996	02/2009	164.36	1050	885.64
180	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	2298.42	2733.86	435.44
181	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	3951.98	4259.48	307.5
182	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	2500	27949	25449
183	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	450	2010	1560
184	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	614.45	451.58
185	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	324.73	1050	725.27
186	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	6093.31	5845.65
187	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	495.44	2980.41	2484.97
188	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	2271.5	3712.5	1441
189	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	RVNL	04/2010	03/2023	2127	2900	773
190	HARIDWAR-LAKSAR	NR	04/2012	N.A.	219.83	346.63	126.8
191	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	03/2020	704.31	1352.74	648.43
192	3RD LINE BETWEEN BHUSAWAL-JALGAON	CR	04/2011	03/2019	184.06	305	120.94
193	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	02/2012	499.96	680.68	180.72
194	HANSDIHA-GODDA NL	ER	04/2011	03/2020	542.18	693.8	151.62
195	TARAKESHWAR-MAGRA NEW BG LINE	ER	04/2010	N.A.	365.17	527.54	162.37
196	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	792.89	1377.48	584.59
197	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	3503.69	3860.4	356.71
198	ETAWAH-MAINPURI (NL), NCR	NCR	04/1997	12/2008	120	346	226

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
199	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	607.09	1425.44	818.35
200	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	12/2017	1185.64	1844.47	658.83
ROAD TRANSPORT AND HIGHWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
201	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	NHAI	12/2003	02/2009	280	525	245
202	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	1108	2967.5	1859.5
203	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	196	655.17	459.17
204	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	199.81	340.14	140.33
205	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	PWD	12/2011	02/2012	156.63	276	119.37
206	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	PWD	03/2012	05/2012	207.03	389.45	182.42
207	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	1266.6	1544	277.4
208	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA	NHAI	03/2018	N.A.	634.7	931.21	296.51
209	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N	NHAI	03/2018	N.A.	2065.96	2169	103.04
210	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF	NHAI	03/2018	N.A.	1029.96	1261.05	231.09
211	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)	NHAI	03/2018	03/2021	1532.62	2499	966.38
212	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF	NHAI	02/2018	N.A.	1052.21	1449	396.79
213	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA	NHAI	02/2018	N.A.	2177.8	2450	272.2
214	SIX-LANING OF BANGALORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT	NHAI	02/2018	N.A.	1995.34	2400	404.66
215	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH	NHAI	02/2018	N.A.	1424.77	1853.42	428.65
216	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	NHAI	03/2017	03/2020	1041.62	1187.1	145.48
217	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	PWD	08/2010	09/2014	186.96	305.61	118.65
218	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH	MORTH	10/2013	03/2017	445.89	653.29	207.4
219	DEVELOPMENT AND OPERATION OF BIKANER-SURATGARH SECTION OF NH-15 BY 2L+PS IN THE STATE OF RAJASTHAN	PWD	03/2009	09/2013	501	671.54	170.54
220	NAGPUR-BIKANER OF NH-11 (2L+PS) UNDER	PWD	01/2012	01/2014	378.07	478.73	100.66

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
	PPP.						
221	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7	PWD	04/2014	08/2017	279.7	398.52	118.82
222	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A 0	PWD	08/2014	11/2017	823.2	937.76	114.56
223	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 0	PWD	08/2014	11/2017	600.87	720.97	120.1
224	FOUR LANNING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4	NHAI	03/2018	N.A.	642.13	807	164.87
225	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	NHAI	03/2017	03/2020	744.64	982	237.36
226	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	NHAI	03/2017	03/2020	1184.71	1310	125.29
227	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	NHAI	11/2012	07/2018	605.84	722.46	116.62
228	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	NHAI	09/2016	08/2019	950.69	1108	157.31
229	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW	NHAI	09/2015	N.A.	771.18	7558	6786.82
230	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	NHAI	08/2016	09/2019	1388.34	2525.8	1137.46
231	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	NHAI	03/2016	04/2019	1587.49	2982	1394.51
232	FOUR LANING OF CHANDIGARH - KHARAR	NHAI	10/2015	12/2017	447.29	746.43	299.14
233	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	1124.11	1232.76	108.65
234	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(0	NHAI	03/2017	03/2020	993.16	1434	440.84
235	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	NHAI	03/2017	03/2020	831.58	1177	345.42
236	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	NHAI	03/2017	03/2020	2064.99	2447	382.01
237	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	1288.07	1420	131.93
238	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	11/2015	1055	1601.77	546.77
239	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	531.13	727	195.87
240	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	PWD	08/2010	10/2010	195.04	377.99	182.95
241	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAF LONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	PWD	11/2010	02/2011	470.2	630.36	160.16
242	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	NHDP	11/2013	05/2017	497.05	881.05	384

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
243	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	MORTH	01/1991	N.A.	675	780.77	105.77
244	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270	NHDP	10/2013	03/2017	445.89	653.29	207.4
245	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	1928.22	2945	1016.78
246	AHMEDABAD TO VADODARA SECTION	NHAI	01/2013	12/2015	2125.24	2521.24	396
247	NASHRI- CHANANI	NHAI	05/2011	06/2015	2159	2519	360
248	BRAHMPUTRA BRIDGE, NH NO-31	NHAI	12/2003	04/2010	217.61	360.84	143.23
249	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	PWD	08/2010	10/2010	193.69	327.92	134.23
250	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	PWD	11/2010	03/2011	624.41	992.67	368.26
251	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	NHAI	12/2003	11/2008	167.64	408.77	241.13
252	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	155.04	255.23	100.19

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
253	JAL MARG VIKAS PROJECT	IWAI	01/2018	03/2023	4200	5369.18	1169.18

STEEL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
254	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	15525	23140	7615

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
255	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	13334	24664	11330

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
256	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCL	05/2005	02/2014	768.88	1113.34	344.46
257	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	1219.21	2000	780.79
258	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	5181.79	5687.79	506
259	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN	CPWD	12/2008	12/2013	114.26	266	151.74

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
	THE STATE OF UTTARA						
260	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	14600	19058	4458
261	REDEVELOPMENT OF EAST KIDWAI NAGAR	NBCC	06/2012	11/2019	4264	4439.23	175.23
262	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	CPWD	02/2014	05/2017	388	488.28	100.28

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
263	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	10151.04	55548.87	45397.83

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(SEPTEMBER 2019)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12/2020	1,2320.00	1,7079.00	4759	48
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	06/2020	1,1459.00	1,6580.00	5121	54
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2021	3492.00	6840.00	3348	133

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2020	314.61	441.33	126.72	21

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
5	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2021	162.76	349.28	186.52	72
6	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	12/2019	5907.11	7080.41	1173.3	48
7	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2024	249.03	448.86	199.83	144
8	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	459.49	307.06	60

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
9	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	02/2022	1112.00	1507.24	395.24	32
10	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)	ONGC	02/2017	05/2021	12/2021	4006.83	4475.92	469.09	7
11	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	02/2021	4497.00	6025.00	1528	26
12	HALDIA LPG IMPORT FACILITY	BPCL	03/2015	10/2018	12/2019	694.00	1097.54	403.54	14
13	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	12/2019	2059.63	2665.65	606.02	57
14	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT	BPCL	11/2014	08/2018	11/2019	4588.29	5245.96	657.67	15

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	KOCHI REFINERY								
15	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	02/2022	2915.00	3049.47	134.47	110
16	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	11/2019	202.94	345.92	142.98	70
17	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	12/2019	861.79	1683.06	821.27	79

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
18	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	12/2020	5111.33	6880.36	1769.03	24
19	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	10/2017	03/2020	1,1846.00	1,2739.82	893.82	29
20	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	08/2021	8692.97	2,1312.11	12619.1	118
21	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	12/2020	4754.42	9072.36	4317.94	24
22	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	10/2019	2496.90	7927.34	5430.44	118
23	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	07/2012	09/2020	5353.00	9996.59	4643.59	98
24	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2021	3919.59	9997.11	6077.52	147
25	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	12/2019	4824.12	5071.94	247.82	86
26	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	01/2018	03/2020	1,1638.55	1,2865.92	1227.37	26
27	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	03/2022	1,1130.19	1,4719.10	3588.91	103
28	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	11/2019	1364.52	1891.41	526.89	43
29	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	01/2021	2978.48	5867.38	2888.9	94
30	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	12/2018	09/2020	1,2532.44	1,3740.53	1208.09	21

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE
(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
31	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	09/2021	1,4366.58	1,5164.05	797.47	27
32	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	02/2022	1381.84	1592.34	210.5	29
33	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	03/2021	1,2964.60	1,7304.00	4339.4	34
34	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	02/2017	06/2020	9750.89	1,2176.28	2425.39	40
35	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2022	2491.58	4397.80	1906.22	114
36	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	10/2019	487.49	639.46	151.97	64
37	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	06/2022	1657.00	5024.35	3367.35	76

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
38	JALANDHAR-PATHANKOT-JAMMU TAWI	NR	03/2002	03/2016	03/2021	625.00	845.58	220.58	60
39	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	12/2022	2288.00	4970.11	2682.11	9
40	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	WR	02/1991	03/2019	03/2020	551.51	809.07	257.56	12
41	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	03/2020	644.78	889.52	244.74	36
42	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM	ECR	04/2016	03/2021	03/2022	731.64	1185.73	454.09	12
43	BONDAMUNDA RANCHI DOUBLING	SER	03/2016	03/2021	12/2021	1724.20	1993.24	269.04	9
44	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	03/2030	1027.40	2373.00	1345.6	324
45	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	03/2020	927.01	1200.00	272.99	12
46	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	03/2021	948.04	1500.00	551.96	12

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE
(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
47	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	06/2022	942.95	1120.00	177.05	39
48	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	09/2022	582.13	1247.64	665.51	6
49	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	06/2020	585.93	1300.44	714.51	16
50	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	SR	02/2015	03/2020	06/2021	760.00	1182.31	422.31	15
51	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	03/2022	744.04	1215.54	471.5	12
52	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	06/2024	2923.13	3791.66	868.53	183
53	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2020	4454.17	1,2524.00	8069.83	108
54	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	03/2020	385.20	1532.00	1146.8	12
55	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	03/2020	532.87	2145.00	1612.13	12
56	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	10/2021	2326.52	4600.00	2273.48	79
57	DAUSA-GANGAPUR CITY(NL),NWR	NWR	02/1997	02/2019	03/2021	410.08	886.41	476.33	25
58	NANGALDAM-TALWARA(NL),NR	NR	03/1981	07/2012	03/2024	450.00	2010.00	1560	140
59	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	NR	03/1995	11/2002	06/2022	2500.00	2,7949.00	25449	235
60	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	03/2025	3951.98	4259.48	307.5	108
61	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	06/2024	810.78	1928.07	1117.29	36
62	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI' - AGASTIYAMPALLI	SR	09/2007	02/2019	02/2020	724.69	2072.50	1347.81	12
63	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	03/2022	2393.47	5021.45	2627.98	96

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE
(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
64	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	03/2020	477.88	751.55	273.67	96
65	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	03/2023	3503.69	3860.40	356.71	12
66	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	03/2022	792.89	1377.48	584.59	12
67	HANSDIHA-GODDA NL	ER	04/2011	03/2020	03/2021	542.18	693.80	151.62	12
68	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	02/2012	03/2025	499.96	680.68	180.72	157
69	3RD LINE BETWEEN BHUSAWAL-JALGAON	CR	04/2011	03/2019	12/2019	184.06	305.00	120.94	9
70	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR	NFR	04/1983	03/2019	03/2020	297.32	614.00	316.68	12
71	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2023	1045.20	2120.16	1074.96	168
72	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	03/2025	1188.91	1619.48	430.57	72
73	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	03/2024	607.09	1425.44	818.35	133
74	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	12/2017	03/2020	1185.64	1844.47	658.83	27
75	RAMGANJMUNDI-BHOPAL (NL), WCR	WCR	04/2001	03/2021	03/2023	424.60	2909.99	2485.39	24
76	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	12/2019	133.41	385.00	251.59	129
77	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	03/2023	03/2024	1856.95	2200.00	343.05	12
78	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	03/2021	287.00	694.00	407	111
79	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	RVNL	04/2010	03/2023	03/2024	2127.00	2900.00	773	12
80	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	03/2022	2271.50	3712.50	1441	12

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE
(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
81	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	MRTP	03/1996	03/2004	03/2021	495.44	2980.41	2484.97	204
82	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2023	247.66	6093.31	5845.65	178
83	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	03/2020	324.73	1050.00	725.27	96
84	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	03/2021	1180.19	4541.00	3360.81	147
85	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	2733.86	435.44	141
86	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	04/2020	12/2020	511.86	1756.92	1245.06	8
87	TIRUCHIRAPPALI-NAGORE-KARAIKKAL (SR) (GC)	SR	09/1995	03/2020	03/2021	303.98	980.00	676.02	12
88	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	03/2021	829.74	1310.23	480.49	12
89	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	03/2022	1111.99	1539.28	427.29	37
90	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	SER	04/2012	12/2016	12/2019	148.77	377.00	228.23	36
91	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	03/2021	1614.59	1870.41	255.82	24
92	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	MRTP	03/2013	03/2016	06/2021	4874.58	8574.97	3700.39	63
93	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	12/2019	06/2020	246.08	348.55	102.47	6
94	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	03/2022	320.66	858.96	538.3	36
95	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	12/2024	2912.96	3845.60	932.64	33
96	ALWAR-BANDIKUI DOUBLING	NWR	04/2013	02/2019	05/2020	242.09	410.00	167.91	15
97	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	12/2018	06/2020	258.20	358.68	100.48	18
98	JAYNAGAR-BIJALPURA INCLUDING	ECR	04/2009	03/2020	03/2022	548.00	819.01	271.01	24

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE
(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	EXTENSION BIJALPURA-BARDIBAS (NEPAL) GC								
99	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	03/2019	03/2020	314.00	728.00	414	12
100	MULTI MODAL TRANSPORT SYSTEM (MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2020	632.68	816.55	183.87	57
101	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	01/2020	295.00	477.31	182.31	12
102	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	03/2019	12/2019	120.70	1800.00	1679.3	9
103	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	ER	04/1987	03/2006	03/2025	406.99	545.70	138.71	228
104	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	03/2025	915.98	2137.81	1221.83	36
105	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	ER	04/2005	03/2017	03/2025	595.51	769.40	173.89	96
106	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	03/2022	701.61	810.02	108.41	40
107	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	03/2023	229.00	860.92	631.92	15

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
108	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	PWD	08/2010	09/2014	12/2019	186.96	305.61	118.65	63
109	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209 (EXISTING CHAINAGE FROM	NHAI	09/2016	08/2019	12/2020	950.69	1108.00	157.31	16
110	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270	NHDP	10/2013	03/2017	09/2019	445.89	653.29	207.4	30
111	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	NHDP	11/2013	05/2017	05/2020	497.05	881.05	384	36
112	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	03/2020	1108.00	2967.50	1859.5	100
113	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	09/2019	1266.60	1544.00	277.4	36
114	4-LANNING OF VARANASI	NHAI	03/2016	04/2019	10/2019	1587.49	2982.00	1394.51	6

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE
(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	GORAKHPUR SECTION OF NH-29 FROM 148.00 TO 208.300 KM [PACKAGE-IV]								
115	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	09/2020	531.13	727.00	195.87	28
116	FOUR LANING OF CHANDIGARH - KHARAR	NHAI	10/2015	12/2017	12/2019	447.29	746.43	299.14	24
117	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH	MORTH	10/2013	03/2017	09/2019	445.89	653.29	207.4	30
118	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	03/2021	1288.07	1420.00	131.93	12
119	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	PWD	11/2010	03/2011	12/2019	624.41	992.67	368.26	105
120	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	PWD	08/2010	10/2010	12/2019	193.69	327.92	134.23	110
121	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	PWD	08/2010	10/2010	06/2020	195.04	377.99	182.95	116
122	4-LANING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	06/2020	1124.11	1232.76	108.65	33
123	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	NHAI	11/2012	07/2018	02/2020	605.84	722.46	116.62	19

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
124	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	07/2020	1,5525.00	2,3140.00	7615	62

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
125	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	05/2020	1,3334.00	2,4664.00	11330	58

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
126	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	10/2019	114.26	266.00	151.74	70
127	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	CPWD	02/2014	05/2017	10/2019	388.00	488.28	100.28	29

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(SEPTEMBER 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
128	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	12/2019	5181.79	5687.79	506	29
129	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	03/2021	1219.21	2000.00	780.79	17

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
130	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	06/2021	1,0151.04	5,5548.87	45397.8	15

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

COR -> Cost Overrun

Details of Ongoing Projects Under -Public Private Partnership Mode

Annexure-XVIII

Costing Rs. 150 Crore and above					(September 2019)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>National Highways Authority Of India</u>							
1	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - PPP (BOT) - [N24000208]	07/2012	291.36 -	291.36	01/2014 -	-	.00	0
2	INDORE-DEWAS(NH-3) - PPP (BOT) - [N24000159]	11/2010	325.00 -	325.00	05/2013 -	-	.00	0
3	2 LANNING OF MOKAMA-MUNGER - PPP (ANNUITY) - [N24000166]	05/2011	351.54 -	351.54	05/2013 -	-	.00	0
4	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - PPP (ANNUITY) - [N24000176]	05/2010	374.00 -	374.00	05/2013 -	-	.00	0
5	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - PPP (ANNUITY) - [N24000177]	09/2011	485.00 -	485.00	08/2013 -	-	.00	0
6	DELHI/ HARYANA BORDER TO ROHTAK - PPP (BOT) - [N24000122]	04/2007	486.00 -	486.00	05/2010 -	03/2020	.00	118
7	2 LANNING OF MUZAFFARPUR - SONBARSA - PPP (ANNUITY) - [N24000188]	05/2011	511.54 -	511.54	11/2013 -	-	.00	0
8	TRICHY - KARUR - PPP (BOT) - [N24000528]	03/2007	516.00 -	516.00	07/2008 -	-	.00	0
9	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - PPP (BOT) - [N24000426]	11/2012	530.07 -	530.07	08/2016 -	12/2019	.00	40
10	TIRUPATI - TIRUTHANI - CHENNAI - PPP (BOT) - [N24000178]	04/2011	571.00 -	571.00	10/2013 -	-	.00	0
11	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - PPP (BOT) - [N24000185]	09/2011	574.00 -	574.00	03/2014 -	-	.00	0
12	4-LANNING OF CHAPRA-HAJIPUR - PPP (ANNUITY) - [N24000187]	01/2011	575.00 -	575.00	07/2013 -	-	.00	0
13	GWALIOR-JHANSI, NH-75 - PPP (ANNUITY) - [N24000089]	12/2003	604.00 -	604.00	12/2009 -	08/2020	.00	128
14	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - PPP (BOT) - [N24000149]	02/2010	617.00 -	617.00	08/2012 -	12/2019	.00	88
15	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - PPP (ANNUITY) - [N24000213]	04/2012	624.00 -	624.00	04/2014 -	-	.00	0
16	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - PPP (BOT) - [N24000586]	06/2016	637.18 -	637.18	06/2019 -	09/2019	.00	3

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above

(September
2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
17	PATNA-MUZZAFFARPUR - PPP (ANNUITY) - [N24000165]	08/2010	671.30 -	671.30	02/2013 -	-	.00	0
18	KRISHNANAGAR-BERHAMPUR - PPP (ANNUITY) - [N24000209]	02/2012	702.16 -	702.16	07/2014 -	06/2020	.00	71
19	MUZZAFFARNAGAR-HARIDWAR - PPP (BOT) - [N24000201]	09/2011	754.00 -	754.00	03/2013 -	12/2019	.00	81
20	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - PPP (BOT) - [N24000587]	06/2016	763.23 -	763.23	06/2019 -	11/2019	.00	5
21	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - PPP (BOT) - [N24000445]	08/2014	822.90 -	822.90	04/2018 -	-	.00	0
22	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION PPP (BOT) - [N24000454]	06/2014	923.04 -	923.04	11/2016 -	05/2020	.00	42
23	KANDLA - MUNDRA PORT - PPP (BOT) - [N24000175]	01/2011	953.88 -	953.88	07/2013 -	-	.00	0
24	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - PPP (BOT) - [N24000453]	01/2015	972.50 -	972.50	07/2017 -	10/2019	.00	27
25	4-LANING OF BRAHMAPORE-FARAKA - PPP (BOT) - [N24000203]	02/2011	998.79 -	998.79	08/2013 -	06/2020	.00	82
26	BAREILLY-SITAPUR (NH-24) - PPP (BOT) - [N24000200]	03/2011	1,046.00 -	1,046.00	09/2013 -	-	.00	0
27	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR PPP (BOT) - [N24000205]	12/2011	1,047.00 -	1,047.00	06/2014 -	03/2019	.00	57
28	4-LANING OF FARAKA-RAIGANJ - PPP (BOT) - [N24000202]	02/2011	1,078.84 -	1,078.84	08/2013 -	12/2019	.00	76
29	SRINAGAL TO BANIHAL - PPP (ANNUITY) - [N24000189]	06/2011	1,100.70 -	1,100.70	06/2014 -	09/2020	.00	75
30	GHAZIABAD-ALIGARH NH-91 - PPP (BOT) - [N24000170]	02/2011	1,141.00 -	1,141.00	08/2013 -	-	.00	0
31	INDORE-JHABUA-GUJRAT/MP - PPP (BOT) - [N24000136]	10/2010	1,175.00 -	1,175.00	04/2013 -	-	.00	0
32	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - PPP (BOT) - [N24000172]	09/2011	1,250.00 -	1,250.00	12/2013 -	06/2020	.00	78
33	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 PPP (BOT) - [N24000230]	05/2013	1,348.20 -	1,348.20	02/2014 -	-	.00	0
34	FOUR LANING OF HOSPET - CHITRADURGA - PPP (BOT) - [N24000490]	03/2015	1,388.00 -	1,388.00	08/2018 -	03/2020	.00	19
35	6-LANING OF DHANKUNI-KHARAGPUR SECTION - PPP (BOT) - [N24000206]	04/2012	1,396.18 -	1,396.18	09/2014 -	12/2019	.00	63
36	PANIKHOLI-RIMOLI - PPP (BOT) - [N24000197]	03/2012	1,410.00 -	1,410.00	09/2014 -	-	.00	0
37	RANCHI-RARGA-JAMSETHPUR - PPP (ANNUITY) - [N24000215]	12/2012	1,479.00 -	1,479.00	06/2015 -	-	.00	0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above

(September 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
38	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - PPP (BOT) - [N24000125]	03/2010	1,509.10	1,509.10	09/2012	-	.00	0
39	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 PPP (BOT) - [N24000183]	11/2011	1,535.00	1,535.00	05/2014	10/2019	.00	65
40	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - PPP (BOT) - [N24000233]	04/2014	1,266.60	1,544.00	09/2016	09/2019	21.90	36
41	ETAWAH CHAKERI - PPP (BOT) - [N24000219]	03/2013	1,573.00	1,573.00	09/2015	-	.00	0
42	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - PPP (BOT) - [N24000505]	06/2015	1,583.79	1,583.79	01/2019	-	.00	0
43	FOUR LANING OF GWALIOR-SHIVPURI - PPP (BOT) - [N24000494]	05/2013	1,055.00	1,601.77	11/2015	-	51.83	0
44	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - PPP (BOT) - [N24000462]	05/2014	1,655.01	1,655.01	08/2016	12/2020	.00	52
45	6 LANING OF AGRA - ETAWAH BYPASS - PPP (BOT) - [N24000452]	07/2015	1,657.20	1,657.20	01/2019	-	.00	0
46	SIX-LANING OF BARWA ADDA-PANAGARH - PPP (BOT) - [N24000515]	04/2014	1,665.00	1,665.00	-	-	.00	0
47	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - PPP (BOT) - [N24000477]	02/2008	1,673.70	1,673.70	10/2011	-	.00	0
48	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - PPP (BOT) - [N24000131]	02/2009	1,693.75	1,693.75	08/2011	-	.00	0
49	PUNE-SATARA(NH-4) - PPP (BOT) - [N24000156]	10/2010	1,724.55	1,724.55	03/2013	12/2019	.00	81
50	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - PPP (ANNUITY) - [N24000163]	07/2010	1,813.76	1,813.76	07/2013	-	.00	0
51	FOUR LANING OF AURANGABAD - YEDISHI - PPP (BOT) - [N24000508]	07/2015	1,871.34	1,871.34	01/2018	12/2019	.00	23
52	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - PPP (BOT) - [N24000232]	11/2013	1,916.79	1,916.79	11/2016	-	.00	0
53	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - PPP (ANNUITY) - [N24000161]	07/2010	1,987.00	1,987.00	07/2015	09/2020	.00	62
54	8 LANING OF MUKARBA CHOWK TO PANIPAT - PPP (BOT) - [N24000449]	07/2015	2,128.72	2,128.72	04/2019	-	.00	0
55	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - PPP BOT (Hybrid Annuity) - [N24001185]	11/2017	2,159.00	2,159.00	01/2019	-	.00	0
56	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - PPP (BOT) - [N24000425]	07/2015	2,288.18	2,288.18	05/2019	-	.00	0
57	4 LANING OF NAGPUR-BETUL - PPP (ANNUITY) - [N24000155]	02/2011	2,498.76	2,498.76	08/2014	-	.00	0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above

(September
2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
58	NASHRI- CHANANI - PPP (ANNUITY) - [N24000162]	05/2011	2,159.00 -	2,519.00	06/2015 -	-	16.67	0
59	AHMEDABAD TO VADODARA SECTION - PPP (BOT) - [N24000222]	01/2013	2,125.24 -	2,521.24	12/2015 -	-	18.63	0
60	VARANASI-AURANGABAD KM.786 TO KM.978.40 - PPP (BOT) - [N24000182]	09/2011	2,848.00 -	2,848.00	03/2014 -	12/2019	.00	69
61	DELHI AGRA APPROVED LENGTH 180.0 KM - PPP (BOT) - [N24000224]	10/2012	1,928.22 -	2,945.00	04/2015 -	-	52.73	0
62	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - PPP (BOT) - [N24000133]	05/2009	1,108.00 -	2,967.50	11/2011 -	03/2020	167.82	100
	Total		75,918.12 -	80,374.57				
	Grand Total		75,918.12	80,374.57				

State-Wise Ongoing Project Detail's

Annexure-XIX

Details of Central Sector Projects Costing Rs.150 crore and above (as on					30.09.2019)
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	<u>A & N ISLANDS</u>				
	<u>Civil Aviation</u>				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	9/2018 (-) [6/2020]	314.61 (-) [441.33]	85.79 (126.72) [21]
	<u>Road Transport And Highways</u>				
2	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N	3/2017	12/2017 (-) [0/0]	409.85 (-) [409.85]	21.11 (0.00) [0]
3	AJANTHA TO BULDHANA	2/2017	7/2019 (-) [7/2019]	401.00 (401.00) [401.00]	98.81 (0.00) [0]
4	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C	3/2015	4/2017 (-) [0/0]	277.17 (-) [277.17]	148.80 (0.00) [0]
5	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (	3/2015	10/2018 (-) [0/0]	262.97 (-) [262.97]	0.00 (0.00) [0]
6	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	11/2017	11/2019 (-) [11/2019]	257.34 (-) [238.00]	41.09 (-19.34) [0]
7	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM	2/2018	10/2018 (-) [0/0]	391.00 (-) [391.00]	22.17 (0.00) [0]
8	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O	3/2018	10/2018 (-) [0/0]	234.27 (-) [234.27]	19.87 (0.00) [0]
9	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00	11/2017	11/2019 (-) [11/2019]	237.80 (-) [238.00]	7.48 (0.20) [0]
	<u>ANDHRA PRADESH</u>				
	<u>Health And Family Welfare</u>				
10	HOSPITAL AND TEACHING- AIIMS GUNTUR	3/2018	/ (-) [2/2020]	601.02 (-) [601.02]	85.04 (0.00) [-]
11	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS- MNAGLAGIRI GUNTUR, ANDHRA PRADESH	8/2017	3/2019 (-) [10/2019]	272.19 (-) [272.19]	140.58 (0.00) [7]
	<u>Information And Broadcasting</u>				
12	FILM AND TELEVISION INSTITUTE ARUNACHAL PRADESH	11/2016	2/2019 (-) [11/2019]	204.32 (-) [204.32]	0.00 (0.00) [9]
	<u>Petroleum</u>				
13	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD	1/2015	3/2021 (-)	342.00 (-)	0.00 (0.00)

	PIPELINE		[3/2021]	[342.00]	[0]
14	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH	8/2018	4/2021 (-) [7/2021]	466.00 (-) [466.00]	84.34 (0.00) [3]
15	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP	8/2017	4/2021 (-) [4/2020]	384.58 (-) [384.58]	85.86 (0.00) [-12]
16	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT	7/2017	2/2021 (-) [2/2021]	580.20 (-) [580.20]	38.21 (0.00) [0]
17	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG	4/2017	9/2018 (9/2019) [9/2019]	420.76 (-) [407.45]	239.45 (-13.31) [12]
18	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	3/2016	6/2020 (-) [8/2021]	34,012.00 (-) [34,012.00]	3,411.92 (0.00) [14]
19	REVAMPING OF FACILITIES AT VIZAG TERMINAL	4/2018	4/2022 (-) [2/2023]	355.00 (-) [355.00]	14.07 (0.00) [10]
20	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM	7/2014	3/2021 (-) [3/2021]	247.00 (-) [247.00]	0.00 (0.00) [0]
21	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP	10/2018	10/2021 (-) [10/2021]	316.20 (-) [316.20]	14.78 (0.00) [0]
22	VISAKH REFINERY MODERNISATION PROJECT	7/2016	7/2020 (-) [7/2020]	20,928.00 (-) [20,928.00]	6,455.02 (0.00) [0]
	<u>Railways</u>				
23	CUMBUM-PRODDATUR	4/2013	/ (-) [0/0]	829.00 (-) [1,599.39]	0.94 (770.39) [0]
24	DUVVADA-VIJAYAWADA	4/2015	/ (-) [0/0]	3,873.07 (-) [3,873.07]	0.38 (0.00) [0]
25	GUDUR-DURGARAJAPATNAM	4/2011	/ (-) [0/0]	761.37 (-) [761.37]	0.52 (0.00) [0]
26	GUNTUR-GUNTAKAL	4/2016	3/2022 (-) [3/2023]	3,631.00 (-) [3,631.00]	407.42 (0.00) [12]
27	KOTLPALLI-NARASAPUR (NL) (SCR)	12/2001	3/2009 (-) [3/2023]	1,045.20 (-) [2,120.16]	412.87 (1,074.96) [168]
28	KOTTAVALSA - KORAPUT DOUBLING	4/2015	3/2022 (-) [3/2022]	2,499.71 (-) [3,382.95]	373.22 (883.24) [0]
29	MULTI MODAL LOGISTICS PARK AT KAKINADA	8/2016	3/2019 (-) [12/2020]	234.50 (-) [235.00]	11.11 (0.50) [21]
30	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM	1/2013	3/2018 (-) [0/0]	387.70 (-) [387.70]	323.91 (0.00) [0]
31	NADIKUDE-SRI KALAHASTI	4/2011	3/2021 (-) [3/2024]	2,288.70 (-) [2,288.70]	667.03 (0.00) [36]
32	NANDYAL-YERRAGUNTALA(NL),SCR	3/1996	2/2009 (-) [0/0]	164.36 (-) [1,050.00]	999.64 (885.64) [0]
33	VIJAYAWADA-GUDUR	4/2015	12/2023 (-)	3,246.26 (-)	1,072.89 (302.41)

			[12/2023]	[3,548.67]	[0]
34	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	3/2012	3/2020 (-) [3/2022]	1,503.71 (-) [1,503.71]	1,563.45 (0.00) [24]
	Road Transport And Highways				
35	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM	12/2017	/ (-) [11/2019]	328.67 (-) [328.67]	176.29 (0.00) [-]
36	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O	12/2017	/ (-) [0/0]	357.00 (-) [357.00]	70.71 (0.00) [0]
37	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA FROM KM 470.415	3/2018	/ (-) [3/2020]	557.30 (-) [557.30]	177.12 (0.00) [-]
38	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216	1/2017	9/2017 (3/2020) [9/2019]	263.45 (-) [263.45]	57.97 (0.00) [24]
39	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V	2/2017	11/2017 (3/2020) [11/2019]	429.43 (-) [429.43]	203.52 (0.00) [24]
40	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1	3/2018	/ (-) [12/2020]	314.43 (-) [314.43]	24.90 (0.00) [-]
41	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD	8/2016	1/2017 (12/2019) [12/2019]	350.61 (-) [350.61]	303.82 (0.00) [35]
42	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C	10/2015	11/2015 (-) [0/0]	333.21 (-) [353.89]	256.11 (20.68) [0]
43	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C	7/2015	12/2015 (-) [0/0]	333.21 (333.21) [333.21]	256.11 (0.00) [0]
44	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0)	7/2015	12/2015 (-) [0/0]	333.21 (-) [333.21]	256.11 (0.00) [0]
45	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12	10/2015	12/2015 (12/2019) [12/2019]	333.21 (-) [355.89]	265.48 (22.68) [48]
46	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)	3/2018	3/2021 (-) [4/2021]	1,532.62 (2,499.00) [2,499.00]	569.15 (966.38) [1]
47	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40)	6/2017	6/2017 (-) [11/2019]	648.33 (-) [306.00]	151.65 (-342.33) [29]
48	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800)	1/2016	11/2018 (-) [0/0]	1,134.97 (-) [1,134.97]	21.73 (0.00) [0]
49	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH	1/2017	1/2018 (3/2020) [1/2020]	576.48 (-) [576.48]	207.93 (0.00) [24]
50	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT	1/2016	8/2016 (3/2020) [3/2020]	348.95 (-) [348.95]	161.18 (0.00) [43]
51	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S	7/2014	2/2015 (-) [0/0]	251.55 (-) [251.55]	7.74 (0.00) [0]
52	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21	1/2016	5/2016 (8/2019) [5/2018]	386.09 (-) [386.09]	182.98 (0.00) [0]
53	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO	11/2016	5/2017 (3/2020)	290.15 (-)	69.47 (0.00)

	69		[3/2020]	[290.15]	[34]
54	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T	1/2014	11/2014 (-) [0/0]	195.45 (-) [195.45]	0.00 (0.00) [0]
55	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS	3/2018	/	565.09	120.20
			(-) [2/2021]	(-) [565.09]	(0.00) [-]
56	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O	3/2016	5/2016 (3/2020) [3/2020]	995.09 (995.00) [995.09]	401.90 (0.00) [46]
57	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216	3/2016	9/2016 (3/2020) [3/2020]	444.84 (-) [444.84]	234.31 (0.00) [42]
58	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2	11/2016	8/2017 (3/2020) [3/2020]	376.25 (-) [376.25]	196.09 (0.00) [31]
59	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (	3/2018	7/2018 (1/2020) [1/2020]	297.12 (294.00) [294.12]	189.72 (-3.00) [18]
60	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG	3/2018	8/2018 (2/2020) [2/2020]	289.67 (290.00) [289.67]	80.77 (0.00) [18]
61	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA	3/2018	11/2018 (5/2020) [5/2020]	504.19 (504.00) [504.19]	201.11 (0.00) [18]
62	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES	3/2015	10/2015 (11/2019) [11/2019]	271.45 (-) [271.45]	152.90 (0.00) [49]
63	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD	1/2017	8/2017 (3/2020) [3/2020]	319.28 (-) [319.28]	103.79 (0.00) [31]
64	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER	3/2017	3/2020 (-) [11/2019]	648.32 (-) [503.10]	497.15 (-145.22) [-4]
65	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU	3/2018	8/2018 (2/2020) [2/2020]	244.95 (245.00) [244.95]	116.71 (0.00) [18]
66	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU	9/2016	2/2017 (12/2019) [12/2019]	372.68 (-) [372.68]	183.25 (0.00) [34]
67	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3	3/2018	8/2018 (3/2020) [3/2020]	228.32 (-) [228.32]	34.74 (0.00) [19]
68	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P	1/2018	8/2018 (8/2020) [8/2020]	418.03 (-) [418.03]	144.09 (0.00) [24]
69	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO	11/2016	1/2018 (1/2020) [1/2020]	378.24 (-) [378.24]	248.70 (0.00) [24]
70	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM	2/2018	/	1,959.00	597.16
			(-) [7/2021]	(-) [1,959.00]	(0.00) [-]
71	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN	12/2017	/	1,323.15	345.33
			(-) [7/2021]	(-) [1,323.15]	(0.00) [-]
72	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG	3/2018	/	1,550.98	569.27
			(-) [7/2021]	(-) [1,550.98]	(0.00) [-]
73	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	11/2011	5/2014 (-) [10/2019]	1,535.00 (-) [1,535.00]	3,220.15 (0.00) [65]

74	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	3/2017	3/2020 (-) [5/2020]	1,041.62 (-) [1,187.10]	778.87 (145.48) [2]
75	TIRUPATI - TIRUTHANI - CHENNAI	4/2011	10/2013 (-) [0/0]	571.00 (-) [571.00]	582.53 (0.00) [0]
76	VIJAYAWADA-GUNDUGOLANU SECTION	9/2014	2/2017 (-) [0/0]	1,684.00 (-) [1,684.00]	54.13 (0.00) [0]
	<u>Steel</u>				
77	CENTRAL DISPATCH YARD	8/2015	8/2018 (10/2019) [10/2019]	320.66 (-) [320.66]	220.91 (0.00) [14]
78	COKE OVEN BATTERY-5	12/2011	12/2017 (10/2019) [10/2019]	2,858.00 (-) [2,500.00]	1,400.76 (-358.00) [22]
	<u>Urban Development</u>				
79	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP	1/2018	3/2019 (-) [0/0]	206.58 (-) [206.58]	82.23 (0.00) [0]
80	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA	7/2014	/ (-) [0/0]	232.00 (-) [232.00]	0.00 (0.00) [0]
81	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD	6/2014	3/2017 (-) [0/0]	157.84 (-) [169.16]	163.98 (11.32) [0]
82	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	8/2007	/ (-) [0/0]	246.90 (-) [246.90]	0.00 (0.00) [0]
	<u>Water Resources</u>				
83	POLAVARAM IRRIGATION PROJECT	2/2009	3/2020 (-) [6/2021]	10,151.04 (-) [55,548.87]	16,417.99 (45,397.83) [15]
	<u>ARUNACHAL PRADESH</u>				
	<u>Power</u>				
84	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009 (10/2019) [10/2019]	2,496.90 (7,927.34) [7,927.34]	7,579.17 (5,430.44) [118]
85	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (-) [0/0]	6,285.33 (-) [19,496.34]	10,989.45 (13,211.01) [0]
	<u>Road Transport And Highways</u>				
86	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN	3/2015	/ (-) [0/0]	172.75 (-) [172.75]	112.43 (0.00) [0]
87	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	3/2015	6/2018 (-) [3/2020]	394.00 (-) [394.00]	272.92 (0.00) [21]
88	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59	3/2015	5/2018 (-) [8/2019]	194.11 (-) [194.11]	178.14 (0.00) [0]
89	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS	10/2015	1/2019 (-) [0/0]	179.82 (-) [179.82]	197.77 (0.00) [0]
90	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX	10/2015	/ (1/2016) [1/2019]	210.50 (210.50) [210.50]	117.06 (0.00) [0]
91	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450 TO KM 605.600(EXISTING CHAINAGE FROM KM.583.450	1/2016	11/2016 (-) [0/0]	183.65 (-) [183.65]	98.02 (0.00) [0]
92	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO	11/2016	/	243.89	30.04

	40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST		(-) [0/0]	(-) [243.89]	(0.00) [0]
93	BORDUMSA NAMCHIK (BURIDEHING - JAIRAMPUR) ROAD ON NH-52B (NEW NH-215) FROM KM. 0.15 (STARTING CHAIN	7/2015	/	189.91	154.43
			(-) [0/0]	(-) [189.91]	(0.00) [0]
94	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 37.500 TO KM	5/2016	/	259.52	155.94
			(-) [0/0]	(-) [259.52]	(0.00) [0]
95	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120.	12/2016	/	200.44	20.03
			(-) [0/0]	(-) [200.44]	(0.00) [0]
96	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50	9/2016	/	568.92	131.32
			(-) [0/0]	(-) [568.92]	(0.00) [0]
97	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5	12/2016	/	188.78	38.37
			(-) [0/0]	(-) [188.78]	(0.00) [0]
98	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	12/2016	1/2017	138.93	72.97
			(-) [1/2020]	(155.00) [155.00]	(16.07) [36]
99	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37	4/2016	/	245.79	98.37
			(-) [9/2020]	(-) [245.79]	(0.00) [-]
100	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM.	4/2016	10/2016	198.00	155.94
			(-) [10/2019]	(-) [198.00]	(0.00) [36]
101	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH	7/2015	10/2018	197.16	66.17
			(9/2015) [9/2018]	(197.16) [197.16]	(0.00) [0]
102	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF	3/2017	/	1,718.59	158.90
			(-) [0/0]	(-) [1,718.59]	(0.00) [0]
103	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	1/2017	3/2017	1,253.10	158.90
			(-) [3/2022]	(-) [1,253.10]	(0.00) [60]
104	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	2/2017	4/2017	167.28	18.94
			(2/2018) [2/2021]	(167.28) [167.28]	(0.00) [46]
105	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS	2/2017	4/2017	216.71	16.40
			(2/2018) [2/2021]	(216.71) [216.71]	(0.00) [46]
106	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K	3/2018	/	392.60	0.00
			(-) [0/0]	(-) [392.60]	(0.00) [0]
107	FUNDED)CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH	11/2015	/	434.06	131.32
			(-) [12/2020]	(-) [434.06]	(0.00) [-]
108	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017	284.09	76.20
			(3/2018) [3/2021]	(284.09) [284.09]	(0.00) [47]
109	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017	195.23	37.30
			(-) [0/0]	(-) [195.23]	(0.00) [0]
110	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	2/2017	4/2017	203.36	49.12
			(-) [0/0]	(-) [203.36]	(0.00) [0]
111	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017	194.66	75.04
			(-) [0/0]	(-) [194.66]	(0.00) [0]
112	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA)	1/2017	4/2017	198.22	24.14
			(-)	(-)	(0.00)

	TO KM.		[0/0]	[198.22]	[0]
113	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	3/2012	5/2012 (6/2018) [0/0]	207.03 (389.45) [389.45]	275.19 (182.42) [0]
114	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	2/2017	4/2017 (2/2018) [2/2021]	180.57 (180.57) [180.57]	13.73 (0.00) [46]
115	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS	2/2017	4/2017 (2/2018) [2/2021]	168.32 (168.32) [168.32]	33.51 (0.00) [46]
116	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	12/2011	2/2012 (-) [0/0]	156.63 (276.00) [276.00]	147.65 (119.37) [0]
117	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P	11/2010	3/2011 (-) [0/0]	305.49 (-) [305.49]	131.08 (0.00) [0]
118	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI	1/2017	/ (-) [0/0]	256.66 (-) [256.66]	24.14 (0.00) [0]
119	TWO-LANING OF JORAM - KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0	2/2017	/ (4/2019) [4/2022]	175.06 (175.06) [175.06]	12.06 (0.00) [-]
120	TWO-LANING OF JORAM - KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1	2/2017	/ (4/2019) [4/2022]	176.12 (176.12) [176.12]	11.82 (0.00) [-]
121	TWO-LANING OF JORAM - KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D	2/2017	/ (2/2018) [2/2021]	199.02 (199.02) [199.02]	9.81 (0.00) [-]
122	TWO-LANING OF JORAM - KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D	2/2017	/ (2/2018) [2/2021]	184.88 (184.88) [184.88]	6.19 (0.00) [-]
123	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU	9/2011	/ (-) [0/0]	1,979.00 (-) [1,979.00]	59.40 (0.00) [0]
	ASSAM				
	Civil Aviation				
124	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	3/2021 (-) [3/2021]	859.86 (-) [860.00]	232.44 (0.14) [0]
	Health And Family Welfare				
125	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021 (-) [10/2021]	875.00 (-) [875.00]	39.27 (0.00) [5]
126	LGBRIMH-TEZPUR, ASSAM	7/2012	12/2014 (-) [0/0]	175.57 (-) [175.57]	113.50 (0.00) [0]
	Petroleum				
127	ASSAM RENEWAL PROJECT FOR GROUP A	3/2009	3/2013 (12/2019) [12/2019]	2,465.15 (-) [2,378.86]	2,147.00 (-86.29) [81]
128	BS VI PROJECT AT GUWAHATI REFINERY	8/2018	2/2020 (-) [2/2020]	557.00 (-) [557.00]	217.83 (0.00) [0]
129	BS-VI PROJECT AT BONGAIGAON REFINERY	5/2018	9/2019 (-) [2/2020]	1,222.00 (-) [1,222.00]	563.53 (0.00) [5]
130	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN	6/2016	8/2020 (-) [8/2020]	224.75 (-) [224.75]	4.37 (0.00) [0]
131	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	7/2011	1/2019 (-)	350.00 (-)	2.06 (0.00)

			[9/2019]	[350.00]	[8]
132	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	6/2010	1/2014 (-) [11/2019]	202.94 (345.92) [345.92]	146.58 (142.98) [70]
133	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	6/2016	8/2019 (-) [9/2019]	423.00 (-) [423.00]	263.70 (0.00) [1]
134	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (-) [6/2020]	543.91 (-) [682.90]	8.97 (138.99) [4]
135	INDMAX PROJECT AT BONGAIGAON REFINERY	2/2016	11/2019 (-) [11/2019]	2,582.00 (-) [2,582.00]	1,557.14 (0.00) [0]
136	PIPELINE NETWORK PROJECT GELEKI, ASSAM	7/2016	5/2020 (-) [5/2020]	249.85 (265.49) [265.49]	157.81 (15.64) [0]
137	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	9/2012	3/2015 (-) [0/0]	871.35 (-) [1,200.00]	565.63 (328.65) [0]
	<u>Railways</u>				
138	AMBARI FALAKATA TO NEW MAYNAGURI	4/2011	3/2019 (-) [3/2020]	314.00 (728.00) [728.00]	704.09 (414.00) [12]
139	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-) [3/2020]	2,232.32 (-) [2,182.00]	654.38 (-50.32) [-24]
140	DIGARU-HOJAI (102 KM)	4/2015	3/2021 (-) [3/2021]	870.96 (-) [2,136.01]	502.44 (1,265.05) [0]
141	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [3/2020]	385.20 (1,532.00) [1,532.00]	629.19 (1,146.80) [12]
	<u>Road Transport And Highways</u>				
142	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (-) [0/0]	268.08 (-) [268.08]	201.56 (0.00) [0]
143	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	11/2010	2/2011 (-) [0/0]	470.20 (-) [630.36]	344.32 (160.16) [0]
144	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS	12/2015	12/2018 (-) [0/0]	225.02 (-) [159.20]	26.00 (-65.82) [0]
145	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	12/2015	6/2018 (-) [0/0]	223.30 (-) [223.30]	78.89 (0.00) [0]
146	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-) [0/0]	520.01 (-) [520.01]	57.36 (0.00) [0]
147	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [0/0]	588.95 (-) [588.95]	366.26 (0.00) [0]
148	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [0/0]	289.99 (-) [289.99]	20.97 (0.00) [0]
149	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (12/2021) [12/2021]	252.00 (-) [252.00]	4.74 (0.00) [71]
150	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	6/2018 (12/2020) [12/2021]	437.39 (-) [437.39]	9.30 (0.00) [42]
151	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END	1/2016	1/2016	294.17	63.00

	OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O		(2/2019) [4/2021]	(-) [294.17]	(0.00) [63]
152	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	4/2010 (-) [7/2019]	217.61 (-) [360.84]	451.15 (143.23) [0]
153	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM	11/2010	2/2014 (-) [12/2019]	197.37 (-) [197.37]	88.86 (0.00) [70]
154	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	5/2008 (-) [6/2019]	160.00 (-) [167.98]	223.81 (7.98) [0]
155	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52	6/2016	1/2019 (-) [0/0]	829.00 (-) [829.00]	343.57 (0.00) [0]
156	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [0/0]	168.39 (-) [168.39]	78.89 (0.00) [0]
157	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE	10/2017	/ (-) [6/2020]	818.00 (-) [818.00]	60.08 (0.00) [-]
158	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DSIGN KM 490.800 TO KM 5	6/2015	6/2018 (1/2021) [12/2021]	463.49 (-) [463.49]	22.32 (0.00) [42]
159	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	3/2015	1/2016 (-) [0/0]	829.00 (-) [829.00]	343.57 (0.00) [0]
160	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (5/2020) [12/2020]	454.89 (-) [454.89]	123.20 (0.00) [31]
161	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	2/2009 (7/2019) [7/2019]	280.00 (456.92) [525.00]	488.37 (245.00) [0]
162	HARANGAJO TO MAIBANG, NH-54	12/2003	7/2009 (10/2018) [10/2018]	196.00 (655.17) [655.17]	655.17 (459.17) [0]
163	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008 (1/2011) [8/2013]	155.04 (255.23) [255.23]	251.39 (100.19) [0]
164	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	4/2009 (3/2011) [8/2019]	199.81 (340.14) [340.14]	319.96 (140.33) [0]
165	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008 (7/2011) [1/2014]	167.64 (408.77) [408.77]	395.78 (241.13) [0]
166	NALBARI T BIJNI (AS-7)	12/2003	4/2008 (-) [3/2020]	208.00 (-) [230.00]	337.76 (22.00) [143]
167	NALBARI TO BIJNI (AS-6)	12/2003	6/2008 (-) [10/2019]	225.00 (-) [225.00]	328.47 (0.00) [136]
168	OUR LANNNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST	3/2017	/ (-) [0/0]	1,049.51 (-) [1,049.51]	86.70 (0.00) [0]
169	SONAPUR TO GUWAHTI (AS-3)	12/2003	3/2008 (-) [8/2020]	245.00 (-) [174.34]	224.28 (-70.66) [149]
170	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ	11/2014	2/2018 (-) [0/0]	218.31 (307.47) [307.47]	256.26 (89.16) [0]
171	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0	9/2018	9/2021 (-)	160.00 (-)	0.50 (0.00)

	AN		[9/2021]	[160.00]	[0]
	<u>BIHAR</u>				
	<u>Civil Aviation</u>				
172	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II	5/2018	10/2022 (-) [10/2022]	539.20 (-) [539.20]	25.64 (0.00) [0]
	<u>Petroleum</u>				
173	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL	5/2016	12/2020 (-) [2/2020]	664.00 (-) [664.00]	601.75 (0.00) [-10]
174	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA	10/2017	10/2022 (-) [10/2022]	359.25 (-) [359.25]	68.16 (0.00) [0]
175	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR	4/2018	3/2021 (-) [3/2021]	522.00 (-) [522.00]	142.71 (0.00) [0]
176	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY	12/2017	10/2020 (-) [10/2020]	199.36 (-) [199.36]	9.39 (0.00) [0]
177	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY	7/2015	11/2018 (-) [8/2019]	822.66 (-) [822.66]	822.02 (0.00) [0]
178	FUEL QUALITY UPGRADATION (NSU,NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY	6/2017	10/2019 (-) [10/2019]	951.64 (-) [951.64]	399.12 (0.00) [0]
179	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY	7/2018	1/2021 (-) [1/2021]	189.00 (-) [189.00]	9.15 (0.00) [0]
180	LPG BP PROJECT MOTIHARI	5/2018	3/2021 (-) [3/2021]	206.50 (-) [206.50]	13.88 (0.00) [0]
181	MOTIHARI AMLEKHGANJ PIPELINE	9/2015	6/2020 (-) [3/2020]	324.00 (-) [324.00]	154.50 (0.00) [-3]
	<u>Power</u>				
182	BARH STPP(3X660MW) NTPC	2/2005	10/2011 (8/2021) [8/2021]	8,692.97 (21,312.11) [21,312.11]	16,453.44 (12,619.14) [118]
183	BRBCL-NABINAGAR TPP- JV (4X250 MW)	1/2007	7/2012 (-) [9/2020]	5,353.00 (-) [9,996.59]	7,918.78 (4,643.59) [98]
184	BUXAR THERMAL POWER PLANT (1320 MW)	3/2019	1/2024 (-) [1/2024]	10,439.09 (10,439.09) [10,439.09]	780.04 (0.00) [0]
185	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	1/2013	5/2018 (12/2021) [3/2021]	12,964.60 (17,304.00) [17,304.00]	13,970.00 (4,339.40) [34]
	<u>Railways</u>				
186	ARA-BHABHUA ROAD (NL)	4/2008	/ (-) [3/2023]	633.87 (-) [633.87]	0.40 (0.00) [-]
187	ARARIA-SUPAUL (NL)	4/2008	/ (3/2023) [3/2023]	1,605.17 (1,605.17) [1,605.17]	23.49 (0.00) [-]
188	BIHTA-AURANGABAD (NL)	4/2008	/ (-) [3/2024]	326.20 (-) [2,995.01]	1.94 (2,668.81) [-]
189	CHHAPRA-MUZAFFARPUR (NL)	4/2006	/ (-) [3/2022]	378.56 (-) [2,609.00]	376.63 (2,230.44) [-]
190	CONSTRUCTION OF ROBS IN THE STATE OF BIHAR	7/2004	12/2007	599.63	0.00

			(-) [0/0]	(674.00) [674.00]	(74.37) [0]
191	CONSTRUCTION OF ROBS IN THE STATE OF BIHAR (NEW ROBS-12)	8/2010	3/2014 (-) [0/0]	400.00 (-) [400.00]	0.00 (0.00) [0]
192	DANIAWAN-BIHARSARIF (NL), ECR	4/2001	/ (-) [0/0]	406.92 (-) [339.00]	200.00 (-67.92) [0]
193	DARBANGHA-KUSHESHWARSTHAN (NL)	4/2005	/ (-) [3/2024]	205.00 (-) [205.00]	5.21 (0.00) [-]
194	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	4/1991	/ (-) [12/2021]	329.39 (803.11) [1,483.14]	1,029.84 (1,153.75) [-]
195	GAYA-DALTONGANJ VIA RAFIGANJ (NL)	4/2008	/ (-) [3/2024]	445.25 (-) [445.25]	1.14 (0.00) [-]
196	HAJIPUR-RAMDAYALUNAGAR DOUBLING	4/2013	/ (-) [1/2020]	213.01 (367.17) [425.17]	406.05 (212.16) [-]
197	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	4/2003	/ (-) [3/2023]	528.65 (2,066.78) [2,066.78]	1,436.88 (1,538.13) [-]
198	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	4/1997	3/2012 (-) [3/2020]	324.73 (898.53) [1,050.00]	1,040.00 (725.27) [96]
199	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	4/2009	3/2020 (-) [3/2022]	548.00 (-) [819.01]	489.11 (271.01) [24]
200	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	4/1997	/ (-) [3/2022]	162.87 (614.45) [614.45]	305.83 (451.58) [-]
201	KISHANGANJ JALALGARH, NL, NEFR	4/2008	/ (3/2022) [3/2022]	333.76 (-) [360.00]	6.67 (26.24) [-]
202	KIUL - GAYA DOUBLING PROJECT	12/2015	3/2020 (-) [10/2021]	1,200.20 (1,200.20) [1,200.20]	397.14 (0.00) [19]
203	KOSI BRIDGE (NL), ECR	4/2002	3/2020 (-) [3/2020]	499.41 (516.02) [516.02]	397.11 (16.61) [0]
204	KURSELA-BIHARIGANJ (NL)	4/2008	/ (-) [3/2024]	192.56 (-) [192.56]	0.39 (0.00) [-]
205	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	4/1996	3/2012 (-) [3/2020]	477.88 (751.55) [751.55]	673.69 (273.67) [96]
206	MOTIHARI-SITAMARHI (NL)	4/2006	/ (-) [3/2024]	211.00 (-) [1,006.00]	24.16 (795.00) [-]
207	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM	4/2016	3/2021 (-) [3/2022]	731.64 (1,185.73) [1,185.73]	32.31 (454.09) [12]
208	MUZAFFARPUR-DARBANGHA (NL)	4/2008	/ (-) [3/2024]	281.30 (-) [281.30]	0.60 (0.00) [-]
209	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL)	4/2008	/ (-) [3/2024]	228.05 (-) [228.05]	1.53 (0.00) [-]
210	MUZAFFARPUR-SITAMARHI NEW LINE	1/1991	7/2014 (-)	332.15 (546.71)	541.07 (214.56)

			[0/0]	[546.71]	[0]
211	NAWADA-LAXMIPUR (NL)	4/2008	/	620.57	0.28
			(-)	(-)	(0.00)
			[3/2024]	[620.57]	[-]
212	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	9/2006	3/2019	532.87	932.80
			(-)	(2,145.00)	(1,612.13)
			[3/2020]	[2,145.00]	[12]
213	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR	4/1998	/	180.82	502.13
			(-)	(726.31)	(545.49)
			[10/2019]	[726.31]	[-]
214	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	12/2015	3/2020	1,491.47	438.38
			(-)	(-)	(0.00)
			[12/2022]	[1,491.47]	[33]
215	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	4/2016	3/2021	744.04	63.74
			(-)	(1,215.54)	(471.50)
			[3/2022]	[1,215.54]	[12]
216	SAKRI-HASANPUR ROAD (NL)	4/1999	/	325.00	362.10
			(-)	(735.20)	(410.20)
			[3/2021]	[735.20]	[-]
217	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	4/2004	/	372.14	777.71
			(-)	(1,470.50)	(1,098.36)
			[3/2021]	[1,470.50]	[-]
218	SAMASTIPUR-DARBANGHA	5/2015	/	380.00	143.36
			(-)	(519.33)	(139.33)
			[2/2023]	[519.33]	[-]
219	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)	4/2008	/	678.62	17.20
			(-)	(-)	(0.00)
			[3/2024]	[678.62]	[-]
	<u>Road Transport And Highways</u>				
220	2 LANNING OF MOKAMA-MUNGER	5/2011	5/2013	351.54	329.40
			(-)	(-)	(0.00)
			[0/0]	[351.54]	[0]
221	2 LANNING OF MUZAFFARPUR - SONBARSA	5/2011	11/2013	511.54	566.60
			(-)	(-)	(0.00)
			[0/0]	[511.54]	[0]
222	2-LANNING WITH PS MOTIHARI-RAXAUL	10/2011	4/2014	375.09	494.33
			(-)	(-)	(0.00)
			[0/0]	[375.09]	[0]
223	4-LANNING OF CHAPRA-HAJIPUR	1/2011	7/2013	575.00	843.67
			(-)	(-)	(0.00)
			[0/0]	[575.00]	[0]
224	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ	5/2015	5/2017	581.84	77.43
			(-)	(-)	(0.00)
			[0/0]	[581.84]	[0]
225	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00	2/2019	/	2,926.42	0.00
			(-)	(-)	(0.00)
			[0/0]	[2,926.42]	[0]
226	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND	9/2018	/	1,478.40	0.00
			(-)	(-)	(0.00)
			[0/0]	[1,478.40]	[0]
227	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE	8/2015	11/2015	288.24	280.00
			(-)	(-)	(0.00)
			[0/0]	[288.24]	[0]
228	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15	12/2017	/	2,598.00	0.00
			(-)	(-)	(0.00)
			[0/0]	[2,598.00]	[0]
229	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE	3/2017	3/2020	235.48	0.00
			(-)	(-)	(-7.71)
			[5/2021]	[227.77]	[14]
230	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH	3/2018	/	496.20	0.00
			(-)	(-)	(0.00)

	PAVED SHOULDER		[0/0]	[496.20]	[0]
231	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	11/2013	7/2016 (-) [0/0]	683.83 (-) [683.83]	596.44 (0.00) [0]
232	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	6/2016 (-) [0/0]	369.77 (-) [369.77]	0.00 (0.00) [0]
233	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016 (-) [0/0]	553.30 (-) [553.30]	267.22 (0.00) [0]
234	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016 (-) [0/0]	178.85 (-) [178.85]	93.11 (0.00) [0]
235	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31	12/2015	/ (-) [12/2019]	1,167.45 (-) [1,167.45]	113.26 (0.00) [-]
236	FOUR LANING OF BHOJPUR TO BUXAR	1/1991	/ (-) [10/2020]	642.41 (-) [642.41]	131.71 (0.00) [-]
237	FOUR LANING OF FORBESGANJ - JOGBANI	8/2015	4/2018 (-) [4/2020]	322.09 (-) [322.09]	77.53 (0.00) [24]
238	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR	1/2014	10/2016 (-) [0/0]	1,408.85 (-) [1,408.85]	753.03 (0.00) [0]
239	FOUR LANING OF KOILWAR TO BHOJPUR	8/2015	/ (-) [1/2020]	814.04 (-) [814.04]	384.48 (0.00) [-]
240	FOUR LANING OF PATNA TO KOILWAR	8/2015	/ (-) [0/0]	556.07 (-) [556.07]	0.00 (0.00) [0]
241	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31	12/2015	4/2019 (-) [0/0]	1,041.10 (-) [1,041.10]	214.34 (0.00) [0]
242	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	9/2011	3/2014 (-) [0/0]	574.00 (-) [574.00]	768.73 (0.00) [0]
243	PATNA-MUZZAFFARPUR	8/2010	2/2013 (-) [0/0]	671.30 (-) [671.30]	885.47 (0.00) [0]
244	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM	8/2016	12/2016 (-) [0/0]	1,742.01 (-) [1,742.01]	719.20 (0.00) [0]
245	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I	1/2018	/ (-) [0/0]	573.70 (-) [573.70]	0.00 (0.00) [0]
246	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH	10/2013	8/2014 (-) [0/0]	278.39 (-) [278.39]	0.00 (0.00) [0]
247	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	1/1991	/ (-) [0/0]	478.35 (-) [478.35]	0.00 (0.00) [0]
248	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	1/1991	/ (-) [0/0]	319.68 (-) [369.77]	113.67 (50.09) [0]
249	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING	2/2014	7/2016 (-) [0/0]	665.50 (-) [665.50]	0.00 (0.00) [0]
250	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	1/1991	8/2016 (-) [0/0]	282.41 (-) [322.01]	278.45 (39.60) [0]

251	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	1/1991	10/2016 (-) [0/0]	358.22 (-) [377.64]	323.60 (19.42) [0]
252	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	1/1991	/ (-) [0/0]	675.00 (-) [780.77]	152.37 (105.77) [0]
253	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHI KM 40	1/1991	/ (-) [0/0]	154.62 (-) [154.62]	0.00 (0.00) [0]
254	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION	1/2018	/ (-) [0/0]	895.39 (-) [895.39]	0.00 (0.00) [0]
255	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	8/2017	8/2017 (-) [2/2022]	950.64 (-) [950.64]	102.51 (0.00) [54]
256	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH	3/2018	/ (-) [0/0]	153.24 (-) [153.24]	2.06 (0.00) [0]
257	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPR	3/2015	7/2016 (-) [0/0]	206.80 (-) [206.80]	74.04 (0.00) [0]
258	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA	8/2015	4/2019 (-) [10/2019]	399.54 (-) [399.54]	195.59 (0.00) [6]
259	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ	8/2015	/ (-) [0/0]	854.80 (-) [854.80]	579.78 (0.00) [0]
260	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR	8/2015	4/2018 (-) [0/0]	516.13 (-) [516.13]	417.09 (0.00) [0]
261	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN	3/2017	3/2020 (-) [3/2020]	672.89 (-) [736.01]	0.00 (63.12) [0]
262	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC	5/2014	8/2016 (-) [12/2020]	199.98 (-) [199.98]	153.43 (0.00) [52]
263	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C	11/2016	10/2019 (-) [10/2019]	230.34 (-) [230.34]	178.39 (0.00) [0]
	<u>Urban Development</u>				
264	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	2/2016	6/2017 (-) [10/2020]	496.18 (496.00) [498.99]	92.22 (2.81) [40]
265	IRRIGATION WORK OF BAGMATI	10/2005	3/2015 (-) [3/2021]	956.00 (-) [956.00]	651.21 (0.00) [72]
	<u>CHHATISGARH</u>				
	<u>Coal</u>				
266	AMERA OC RCE	2/2015	3/2018 (-) [3/2020]	335.97 (-) [335.97]	51.25 (0.00) [24]
267	AMGAON OPENCAST PROJECT RCE	7/2015	3/2020 (-) [3/2020]	316.10 (-) [316.10]	73.31 (0.00) [0]
268	BAROUD OC EXPANSION (RCE)- 3MTY	4/2012	3/2016 (-) [3/2020]	258.56 (-) [258.56]	180.07 (0.00) [48]
269	BIJARI OC RCE (1.50 MTY)	5/2014	3/2020 (-) [3/2020]	164.49 (-) [164.49]	82.91 (0.00) [0]
270	CHHAL OC SEAM -III (6.00 MTY)	12/2013	3/2022	610.63	102.91

			(-) [3/2022]	(-) [610.63]	(0.00) [0]
271	DURGAPUR OPENCAST PROJECT	2/2015	3/2023 (-) [3/2023]	916.24 (-) [916.24]	4.02 (0.00) [0]
272	GEVRA EXPANSION OCP (SECL) (35-70) MTY	6/2010	3/2023 (-) [3/2023]	11,816.40 (-) [11,816.40]	2,882.36 (0.00) [0]
273	JAGANNATHPOR OCP(3.00MTY)	9/2008	3/2015 (-) [3/2020]	152.43 (-) [459.49]	193.40 (307.06) [60]
274	JHIRIA WEST OPENCAST PROJECT	11/2018	3/2026 (-) [3/2026]	389.97 (-) [389.97]	0.00 (0.00) [0]
275	KARTALI (EAST) OCP (2.50 MTY)	7/2008	3/2014 (-) [3/2020]	178.44 (-) [178.44]	2.88 (0.00) [72]
276	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY	8/2013	3/2023 (-) [3/2023]	7,612.33 (-) [7,612.33]	2,057.57 (0.00) [0]
277	MADANNAGAR OPENCAST PROJECT	10/2015	3/2024 (-) [3/2024]	1,875.32 (-) [1,875.32]	0.00 (0.00) [0]
278	MAHAMAYA OPENCAST PROJECT	5/2018	3/2026 (-) [3/2026]	410.26 (-) [410.26]	9.53 (0.00) [0]
279	MANIKPUR OC EXPANSION (3.5 MTY)	12/2009	3/2014 (-) [3/2021]	321.50 (-) [321.50]	192.55 (0.00) [84]
280	PELMA OCP(15.00MTY)	11/2014	3/2023 (-) [3/2023]	1,624.59 (-) [1,624.59]	6.42 (0.00) [0]
281	VIJAY WEST OPENCAST PROJECT	5/2017	3/2026 (-) [3/2026]	976.95 (-) [976.95]	75.96 (0.00) [0]
	<u>Petroleum</u>				
282	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH	12/2016	4/2021 (-) [0/0]	300.00 (-) [300.00]	1.09 (0.00) [0]
	<u>Power</u>				
283	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	12/2012	10/2017 (3/2020) [3/2020]	11,846.00 (-) [12,739.82]	12,457.15 (893.82) [29]
284	TALAIALLI COAL MINING PROJECT	9/2015	11/2019 (-) [11/2019]	3,004.00 (-) [3,004.00]	1,610.00 (0.00) [0]
	<u>Railways</u>				
285	CHAMPA-JHARSUGUDA 3RD LINE	4/2008	12/2019 (10/2019) [10/2019]	872.00 (1,226.51) [1,226.51]	1,044.67 (354.51) [-2]
286	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUK DIVISION OF SEC RAILW	2/2016	3/2020 (-) [3/2020]	393.98 (-) [393.98]	241.23 (0.00) [0]
287	GEVRA ROAD PENDRA ROAD	2/2014	3/2022 (-) [12/2022]	2,288.00 (-) [4,970.11]	619.50 (2,682.11) [9]
288	JHARSUGUDA-BILASPUK 4TH LINE	4/2015	3/2021 (12/2022) [12/2022]	1,973.00 (1,973.66) [1,973.66]	139.42 (0.66) [21]
289	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	4/2013	9/2018 (-)	3,055.00 (-)	1,729.64 (0.00)

			[12/2020]	[3,055.00]	[27]
290	KIRANDUL - JAGDALPUR DOUBLING	12/2012	3/2020 (-) [3/2023]	1,160.00 (-) [1,160.83]	682.29 (0.83) [36]
291	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR	5/2014	3/2018 (-) [0/0]	207.00 (-) [207.00]	153.83 (0.00) [0]
292	RAIPUR - TITLAGARH - DOUBLING	3/2007	3/2020 (-) [6/2020]	1,402.02 (-) [1,100.00]	1,050.36 (-302.02) [3]
	<u>Road Transport And Highways</u>				
293	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF	3/2018	/ (3/2021) [3/2021]	1,029.96 (-) [1,261.05]	97.55 (231.09) [-]
294	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1)	12/2015	4/2018 (3/2020) [3/2020]	726.67 (598.13) [598.13]	414.73 (-128.54) [23]
295	FOUR LANING OF SARAGAON - BILASPUR	12/2015	4/2018 (8/2018) [8/2018]	509.13 (-) [509.13]	412.66 (0.00) [0]
296	FOUR LANING OF SIMGA - SARAGAON	12/2015	5/2018 (10/2019) [10/2019]	596.67 (-) [596.67]	392.06 (0.00) [17]
297	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION.	12/2015	/ (-) [0/0]	291.05 (-) [291.05]	181.90 (0.00) [0]
298	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION	11/2015	12/2015 (-) [0/0]	485.44 (-) [485.44]	445.75 (0.00) [0]
	<u>Steel</u>				
299	NMDC INTEGRATED STEEL PLANT	1/2010	5/2015 (7/2020) [7/2020]	15,525.00 (-) [23,140.00]	16,064.29 (7,615.00) [62]
	<u>D & N HAVELI</u>				
	<u>Petroleum</u>				
300	DAMAN DEVELOPMENT PROJECT	8/2014	5/2019 (10/2019) [10/2019]	6,086.08 (5,842.31) [5,842.31]	4,784.88 (-243.77) [5]
	<u>DELHI</u>				
	<u>Civil Aviation</u>				
301	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	11/2016	4/2020 (-) [12/2020]	233.38 (-) [233.38]	84.73 (0.00) [8]
	<u>Health And Family Welfare</u>				
302	AIIMS - MOTHER AND CHILD BLOCK	12/2013	5/2017 (-) [9/2019]	204.44 (-) [204.44]	188.00 (0.00) [28]
303	AIIMS - OPD(NEW)	8/2014	5/2017 (-) [0/0]	293.65 (-) [293.65]	290.71 (0.00) [0]
304	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	/ (-) [2/2020]	156.56 (-) [156.65]	54.94 (0.09) [-]
305	LHMC NEW DELHI-RE-DEVELOPMENT	2/2013	11/2013 (-) [10/2020]	414.11 (-) [513.89]	147.00 (99.78) [83]
	<u>Heavy Industry</u>				
306	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	8/2016	9/2019 (-) [9/2019]	1,554.00 (-) [1,554.00]	335.03 (0.00) [0]
	<u>Power</u>				

307	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	3/2015	5/2017 (-) [12/2019]	1,394.52 (-) [1,394.52]	427.71 (0.00) [31]
	<u>Railways</u>				
308	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE	4/2012	/	295.68	79.53
			(-) [3/2023]	(-) [295.68]	(0.00) [-]
309	GRADE SEPERATOR AT DAYABASTI	4/1999	/	156.65	107.86
			(-) [3/2024]	(-) [197.17]	(40.52) [-]
	<u>Road Transport And Highways</u>				
310	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW	9/2015	/	771.18	261.77
			(-) [0/0]	(-) [7,558.00]	(6,786.82) [0]
311	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8	7/2017	9/2019	269.69	0.00
			(-) [12/2019]	(-) [269.69]	(0.00) [3]
	<u>Telecommunications</u>				
312	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	6/2016	6/2017	418.26	367.03
			(-) [0/0]	(-) [418.26]	(0.00) [0]
	<u>Urban Development</u>				
313	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	6/2015	4/2019	197.33	48.86
			(-) [11/2020]	(-) [197.33]	(0.00) [19]
314	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI	7/2017	/	218.72	0.00
			(-) [0/0]	(-) [218.72]	(0.00) [0]
315	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	7/2012	12/2015	884.30	703.90
			(-) [0/0]	(-) [884.30]	(0.00) [0]
316	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	10/2017	11/2019	271.90	33.56
			(-) [11/2019]	(-) [271.90]	(0.00) [0]
317	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU	12/2017	6/2019	188.00	146.45
			(-) [0/0]	(-) [188.00]	(0.00) [0]
318	DELHI MRTS PHASE-III	9/2011	3/2016	38,585.00	34,763.00
			(-) [0/0]	(-) [38,585.00]	(0.00) [0]
319	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	10/2019	1,219.21	374.71
			(-) [3/2021]	(-) [2,000.00]	(780.79) [17]
320	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B	11/2017	5/2020	238.56	63.42
			(-) [5/2020]	(-) [238.56]	(0.00) [0]
321	REDEVELOPMENT OF EAST KIDWAI NAGAR	6/2012	11/2019	4,264.00	3,246.53
			(-) [11/2019]	(-) [4,439.23]	(175.23) [0]
322	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N	10/2016	/	392.00	12.56
			(8/2020) [3/2021]	(-) [392.00]	(0.00) [-]
323	REDEVELOPMENT OF GPRA AT MOHAMMADPUR	10/2016	/	422.00	14.20
			(-) [12/2020]	(-) [422.00]	(0.00) [-]
324	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR	7/2016	/	2,694.00	0.00
			(-) [0/0]	(-) [2,694.00]	(0.00) [0]
325	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	10/2016	4/2018	248.20	33.39
			(-) [0/0]	(-) [248.20]	(0.00) [0]

	<u>GOA</u>				
	<u>Health And Family Welfare</u>				
326	SUPER SPECIALITY BLOCK PMSSY GOA	1/2018	/ (-) [5/2020]	249.01 (-) [249.01]	73.40 (0.00) [-]
	<u>Road Transport And Highways</u>				
327	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE	3/2015	/ (-) [0/0]	280.16 (-) [290.59]	280.47 (10.43) [0]
328	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD	3/2015	/ (-) [0/0]	184.05 (-) [184.05]	91.39 (0.00) [0]
329	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE	10/2015	/ (-) [0/0]	936.40 (-) [936.40]	262.25 (0.00) [0]
330	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K	3/2015	/ (-) [0/0]	298.33 (-) [298.33]	153.33 (0.00) [0]
331	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDEAPAR BRIDGE	3/2015	4/2018 (-) [0/0]	297.00 (-) [297.00]	290.64 (0.00) [0]
332	KARASWADA TO BAMBOLIM	3/2017	12/2019 (-) [12/2019]	852.67 (852.67) [852.67]	108.04 (0.00) [0]
333	PATRADEVI TO KARASWADA 4L	3/2017	5/2020 (-) [5/2020]	634.32 (634.32) [634.32]	102.33 (0.00) [0]
334	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER	12/2015	/ (-) [0/0]	773.98 (-) [773.98]	259.46 (0.00) [0]
335	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR	12/2015	/ (-) [0/0]	819.95 (-) [819.95]	191.63 (0.00) [0]
	<u>GUJARAT</u>				
	<u>Atomic Energy</u>				
336	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015 (-) [6/2020]	11,459.00 (16,580.00) [16,580.00]	14,137.00 (5,121.00) [54]
	<u>Petroleum</u>				
337	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT	3/2018	/ (-) [8/2022]	588.20 (-) [588.20]	0.94 (0.00) [-]
338	BS-VI PROJECT AT GUJARAT REFINERY	3/2018	9/2019 (-) [3/2020]	3,380.00 (-) [3,380.00]	2,102.63 (0.00) [6]
339	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	4/2016	4/2018 (-) [10/2019]	327.78 (-) [200.00]	146.50 (-127.78) [18]
340	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY	8/2017	8/2020 (-) [8/2020]	1,342.00 (-) [1,342.00]	6.30 (0.00) [0]
341	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE	10/2017	2/2020 (-) [10/2020]	906.00 (-) [906.00]	93.08 (0.00) [8]
342	GAS COMPRESSOR PROJECT AT ANKLESHWAR ASSET (GCP-ANK)	10/2018	3/2021 (-) [3/2021]	156.67 (-) [156.67]	0.00 (0.00) [0]
343	INFRASTRUCTURE DEVLOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY	9/2016	7/2020 (-) [7/2020]	208.35 (-) [208.35]	123.99 (0.00) [0]
344	REDEVELOPMENT OF SANTHAL FIELD	2/2017	3/2026	1,162.56	392.39

			(-) [3/2026]	(-) [1,162.56]	(0.00) [0]
345	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI	9/2018	2/2021 (-) [2/2021]	225.54 (-) [225.54]	1.41 (0.00) [0]
	<u>Power</u>				
346	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT	12/2017	6/2019 (-) [12/2019]	193.14 (-) [193.14]	97.26 (0.00) [6]
347	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT	5/2017	9/2018 (-) [12/2019]	175.64 (-) [175.64]	100.00 (0.00) [15]
	<u>Railways</u>				
348	AHMEDABAD-BOTAD (GC)	4/2012	12/2021 (-) [12/2021]	975.62 (-) [1,082.32]	994.30 (106.70) [0]
349	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	4/2008	3/2020 (3/2021) [3/2021]	829.74 (1,215.34) [1,310.23]	1,394.73 (480.49) [12]
350	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	4/2006	3/2011 (3/2017) [3/2017]	117.36 (196.95) [202.35]	809.40 (84.99) [0]
351	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	2/1991	3/2019 (3/2020) [3/2020]	551.51 (809.07) [809.07]	616.90 (257.56) [12]
352	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	4/2008	3/2012 (3/2022) [3/2022]	318.24 (321.62) [321.62]	125.76 (3.38) [120]
353	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM	4/2017	3/2020 (3/2021) [3/2021]	691.84 (663.29) [663.29]	166.84 (-28.55) [12]
354	DHASA-JETALSAR (GC)	4/2012	3/2021 (-) [3/2021]	644.38 (-) [644.38]	352.02 (0.00) [0]
355	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO	3/2017	/ (-) [0/0]	243.60 (-) [243.60]	0.00 (0.00) [0]
356	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC)	4/2011	/ (3/2021) [3/2021]	844.10 (844.10) [844.10]	97.74 (0.00) [-]
357	MULTI MODAL LOGISTICS PARK AT VARNAMA	10/2013	3/2019 (-) [12/2019]	343.00 (-) [343.00]	222.83 (0.00) [9]
358	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220	3/2012	/ (-) [0/0]	153.83 (-) [153.83]	0.00 (0.00) [0]
359	PALANPUR-SAMAKHAYALI (DL)	4/2013	12/2021 (-) [3/2022]	1,548.66 (-) [1,548.66]	1,268.31 (0.00) [3]
360	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	4/1994	3/2019 (3/2022) [3/2022]	320.66 (858.56) [858.96]	534.00 (538.30) [36]
361	SURENDRA NAGAR RAJKOT	4/2015	3/2021 (3/2021) [3/2021]	1,002.39 (1,002.39) [1,002.39]	378.38 (0.00) [0]
362	VIRAMGAM-SAMAKHIALI (DL)	4/2011	3/2021 (3/2022) [3/2022]	1,037.15 (1,037.15) [1,037.15]	992.18 (0.00) [12]
363	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON	3/2012	/ (-) [0/0]	248.26 (-) [248.26]	0.00 (0.00) [0]

	Road Transport And Highways				
364	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION	12/2016	/	417.19	262.83
			(-)	(-)	(0.00)
			[9/2019]	[417.19]	[-]
365	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000	7/2016	/	829.97	75.08
			(-)	(-)	(0.00)
			[1/2020]	[829.97]	[-]
366	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT	6/2017	6/2020	1,958.88	1,116.85
			(-)	(-)	(0.00)
			[8/2020]	[1,958.88]	[2]
367	AHMEDABAD TO VADODARA SECTION	1/2013	12/2015	2,125.24	4,659.71
			(-)	(2,521.24)	(396.00)
			[0/0]	[2,521.24]	[0]
368	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS	5/2016	/	364.56	240.57
			(-)	(-)	(27.44)
			[12/2019]	[392.00]	[-]
369	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR	3/2018	/	1,161.39	0.00
			(11/2021)	(1,404.00)	(0.00)
			[0/0]	[1,161.39]	[0]
370	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S	3/2018	/	1,437.64	457.31
			(12/2018)	(1,687.00)	(0.00)
			[7/2021]	[1,437.64]	[-]
371	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S	3/2018	/	2,702.05	0.00
			(-)	(-)	(0.00)
			[1/2021]	[2,702.05]	[-]
372	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA	10/2018	5/2019	400.76	4.45
			(-)	(-)	(0.00)
			[0/0]	[400.76]	[0]
373	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU	8/2017	3/2018	962.43	45.70
			(-)	(-)	(0.00)
			[0/0]	[962.43]	[0]
374	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE	12/2017	11/2018	867.97	90.63
			(-)	(-)	(0.00)
			[0/0]	[867.97]	[0]
375	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6.	5/2016	/	998.18	435.25
			(-)	(-)	(0.00)
			[0/0]	[998.18]	[0]
376	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST	5/2016	/	723.64	321.67
			(-)	(-)	(0.00)
			[9/2019]	[723.64]	[-]
377	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR	5/2016	/	834.64	140.44
			(-)	(-)	(0.00)
			[10/2019]	[834.64]	[-]
378	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU	5/2016	/	763.08	357.12
			(-)	(-)	(0.00)
			[0/0]	[763.08]	[0]
379	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	3/2010	9/2012	1,509.10	3,669.10
			(12/2019)	(3,787.21)	(0.00)
			[0/0]	[1,509.10]	[0]
380	JUNAGADH BYPASS	10/2017	10/2017	232.49	0.00
			(-)	(-)	(0.00)
			[11/2019]	[232.49]	[25]
381	KANDLA - MUNDRA PORT	1/2011	7/2013	953.88	976.79
			(-)	(-)	(0.00)
			[0/0]	[953.88]	[0]
382	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF	2/2018	/	1,052.21	1,296.87
			(-)	(1,449.00)	(396.79)
			[1/2021]	[1,449.00]	[-]
383	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG.	1/2017	/	1,251.11	1,084.26
			(-)	(-)	(0.00)
			[1/2021]	[1,251.11]	[-]

384	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME	5/2016	/ (-) [0/0]	425.60 (241.41) [425.60]	97.78 (0.00) [0]
385	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4	3/2018	6/2021 (-) [6/2021]	351.00 (-) [351.00]	0.48 (0.00) [0]
386	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEEN	3/2018	11/2018 (-) [0/0]	464.07 (-) [464.07]	14.17 (0.00) [0]
387	UPGRADATION TO 2 LANE WITH PAVED SHOULDER WITH RIGID PAVEMENTS FROM 37/400 TO KM 66/700 ON NH 848 ON	3/2016	2/2016 (-) [0/0]	208.34 (-) [208.34]	112.87 (0.00) [0]
388	VADODARA-SURAT SECTION	3/2014	8/2016 (-) [0/0]	503.16 (-) [503.16]	389.50 (0.00) [0]
389	WIDENING FROM TWO LANE TO FOUR LANE WITH PAVED SHOULDER AND STRENGTHNING OF EXISTING PAVEMENT BETWEEN	3/2016	2/2017 (-) [0/0]	223.67 (-) [223.67]	112.81 (0.00) [0]
	<u>Urban Development</u>				
390	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	12/2018 (-) [7/2020]	10,773.00 (-) [10,773.00]	6,057.03 (0.00) [19]
391	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT	1/2013	/ (-) [0/0]	175.00 (-) [175.00]	1.83 (0.00) [0]
	<u>HARYANA</u>				
	<u>Fertilisers</u>				
392	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT	1/2018	11/2019 (-) [11/2019]	215.92 (-) [215.92]	117.03 (0.00) [0]
	<u>Health And Family Welfare</u>				
393	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	9/2014	3/2018 (-) [0/0]	505.58 (-) [523.00]	508.29 (17.42) [0]
	<u>Petroleum</u>				
394	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY	1/2019	1/2021 (-) [1/2021]	909.00 (-) [909.00]	16.17 (0.00) [0]
395	BS-VI PROJECT AT PANIPAT REFINERY	12/2017	7/2019 (-) [12/2019]	3,529.00 (-) [3,529.00]	1,720.28 (0.00) [5]
396	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	4/2018	2/2020 (-) [2/2020]	206.63 (-) [206.63]	13.75 (0.00) [0]
397	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA	11/2017	11/2020 (-) [11/2020]	255.00 (-) [255.00]	75.50 (0.00) [0]
398	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY	10/2018	2/2020 (-) [2/2020]	598.00 (-) [598.00]	15.22 (0.00) [0]
399	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT	12/2018	6/2021 (-) [6/2021]	278.60 (-) [278.60]	0.00 (0.00) [0]
400	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT	8/2018	8/2020 (-) [8/2020]	1,636.00 (-) [1,636.00]	148.87 (0.00) [0]
401	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT	8/2018	8/2020 (9/2020) [9/2020]	286.42 (-) [286.42]	1.93 (0.00) [1]
	<u>Railways</u>				
402	MULTI MODAL LOGISTICS PARK AT BARHI	12/2015	3/2019	346.32	286.78

			(-) [3/2020]	(-) [346.32]	(0.00) [12]
403	ROHTAK-MEHAM HANSI	4/2012	12/2011 (-) [3/2021]	287.00 (-) [694.00]	220.42 (407.00) [111]
	<u>Road Transport And Highways</u>				
404	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	12/2015	6/2016 (-) [9/2019]	602.95 (507.70) [507.70]	495.63 (-95.25) [39]
405	4 LANING OF AMBALA - KAITHAL - PACKAGE -2	1/2016	7/2018 (-) [10/2019]	574.28 (537.16) [537.16]	500.61 (-37.12) [15]
406	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL	3/2017	3/2020 (-) [9/2019]	639.79 (-) [552.90]	491.93 (-86.89) [6]
407	8 LANING OF MUKARBA CHOWK TO PANIPAT	7/2015	4/2019 (-) [0/0]	2,128.72 (-) [2,128.72]	971.24 (0.00) [0]
408	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC)	1/2017	3/2019 (7/2019) [0/0]	276.01 (-) [276.01]	187.39 (0.00) [0]
409	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS	1/2017	3/2019 (3/2020) [9/2019]	247.25 (-) [247.25]	144.71 (0.00) [6]
410	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73	8/2016	5/2019 (-) [12/2019]	248.97 (-) [248.97]	240.44 (0.00) [7]
411	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P	3/2018	/ (-) [12/2020]	1,484.30 (-) [1,484.30]	45.34 (0.00) [-]
412	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211	9/2016	5/2019 (-) [2/2019]	1,004.67 (-) [813.45]	576.86 (-191.22) [0]
413	DELHI/ HARYANA BORDER TO ROHTAK	4/2007	5/2010 (-) [3/2020]	486.00 (-) [486.00]	470.01 (0.00) [118]
414	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2	11/2015	5/2018 (-) [0/0]	867.66 (-) [867.66]	502.66 (0.00) [0]
415	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I	8/2015	2/2018 (-) [0/0]	723.54 (-) [723.54]	530.94 (0.00) [0]
416	ISMAILABAD-NARNAUL PKG-1	1/2019	/ (-) [0/0]	996.65 (-) [996.65]	286.25 (0.00) [0]
417	ISMAILABAD-NARNAUL PKG-2	1/2019	/ (-) [0/0]	1,243.45 (-) [1,243.45]	338.76 (0.00) [0]
418	ISMAILABAD-NARNAUL PKG-3	1/2019	/ (-) [0/0]	889.36 (-) [889.36]	251.12 (0.00) [0]
419	ISMAILABAD-NARNAUL PKG-4	1/2019	/ (-) [0/0]	1,018.79 (-) [1,018.79]	226.52 (0.00) [0]
420	ISMAILABAD-NARNAUL PKG-5	1/2019	/ (-) [0/0]	1,051.91 (-) [1,051.91]	213.77 (0.00) [0]
421	ISMAILABAD-NARNAUL PKG-6	1/2019	/ (-) [0/0]	1,120.06 (-) [1,120.06]	228.51 (0.00) [0]
422	ISMAILABAD-NARNAUL PKG-7	1/2019	/	1,137.42	305.25

			(-) [0/0]	(-) [1,137.42]	(0.00) [0]
423	ISMAILABAD-NARNAUL PKG-8	1/2019	/	1,033.19	209.38
			(-) [0/0]	(-) [1,033.19]	(0.00) [0]
424	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	5/2009	11/2011	1,108.00	3,986.72
			(-) [3/2020]	(2,967.50) [2,967.50]	(1,859.50) [100]
425	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS	3/2018	/	551.58	243.38
			(-) [3/2020]	(-) [551.58]	(0.00) [-]
426	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE	3/2018	/	275.12	119.66
			(-) [3/2020]	(-) [275.12]	(0.00) [-]
427	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTING	3/2018	/	307.79	140.10
			(-) [3/2020]	(-) [307.79]	(0.00) [-]
428	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN	3/2018	/	181.78	52.50
			(-) [6/2020]	(-) [181.78]	(0.00) [-]
429	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN	3/2018	/	198.05	87.04
			(-) [3/2020]	(-) [198.05]	(0.00) [-]
430	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I)	3/2018	/	795.50	80.90
			(-) [7/2021]	(-) [799.30]	(3.80) [-]
431	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA	3/2018	/	634.70	2.55
			(-) [7/2021]	(931.21) [931.21]	(296.51) [-]
	HIMACHAL PRADESH				
	Health And Family Welfare				
432	AIIMS BILASPUR	4/2018	9/2021	1,351.00	137.87
			(-) [9/2021]	(-) [1,351.00]	(0.00) [0]
	Petroleum				
433	BRANCH PIPELINE OF PAJPL TO UNA	2/2016	9/2019	151.00	147.35
			(-) [0/0]	(-) [151.00]	(0.00) [0]
	Power				
434	PARBATI HEP (4X200 MW) (NHPC) II	9/2002	9/2009	3,919.59	7,642.51
			(-) [12/2021]	(-) [9,997.11]	(6,077.52) [147]
	Railways				
435	BHANUPALI-BILASPUR BERI NL	4/2008	12/2026	2,966.99	398.76
			(-) [12/2025]	(-) [7,000.00]	(4,033.01) [-12]
	Road Transport And Highways				
436	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345)	2/2016	2/2019	273.20	267.38
			(-) [6/2019]	(-) [273.20]	(0.00) [0]
437	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P	6/2017	6/2020	2,485.93	704.29
			(-) [9/2021]	(-) [2,485.93]	(0.00) [15]
438	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM)	11/2013	11/2016	1,916.79	1,948.92
			(-) [0/0]	(-) [1,916.79]	(0.00) [0]
439	FOUR LANING OF PARWANOO -SOLAN	9/2015	3/2018	934.46	531.34
			(-) [3/2020]	(1,302.98) [934.46]	(0.00) [24]
440	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC	3/2018	/	478.74	15.06
			(-)	(1,071.75)	(0.00)

	M		[5/2021]	[478.74]	[-]
441	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH	9/2016	/ (-) [7/2020]	1,273.71 (-) [1,273.71]	0.00 (0.00) [-]
442	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000)	10/2016	/ (-) [11/2019]	447.75 (-) [447.75]	179.17 (0.00) [-]
443	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS	8/2016	/ (-) [9/2020]	1,583.18 (2,170.44) [1,583.18]	234.67 (0.00) [-]
	<u>Urban Development</u>				
444	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	11/2012	11/2014 (-) [10/2019]	270.83 (-) [270.83]	199.91 (0.00) [59]
	<u>JAMMU AND KASHMIR</u>				
	<u>Civil Aviation</u>				
445	CONSTRUCTION OF TERMINAL BUILDING & ASSOCIATED WORKS AT LEH AIRPORT	7/2018	9/2021 (-) [9/2021]	323.19 (-) [323.19]	10.14 (0.00) [0]
	<u>Power</u>				
446	KIRU HYDRO ELECTRIC PROJECT	3/2019	/ (-) [0/0]	4,287.59 (-) [4,287.59]	0.00 (0.00) [0]
	<u>Railways</u>				
447	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	3/1995	11/2002 (-) [6/2022]	2,500.00 (27,949.00) [27,949.00]	19,403.28 (25,449.00) [235]
	<u>Road Transport And Highways</u>				
448	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE	12/2017	/ (-) [1/2021]	1,471.75 (1,339.00) [1,339.00]	376.15 (-132.75) [-]
449	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A	12/2015	6/2019 (-) [12/2020]	2,168.66 (-) [2,168.66]	621.26 (0.00) [18]
450	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A	12/2015	12/2018 (12/2019) [7/2020]	2,136.97 (2,273.00) [2,136.97]	1,214.48 (0.00) [19]
451	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	7/2010	7/2013 (-) [0/0]	1,813.76 (-) [1,813.76]	2,393.99 (0.00) [0]
452	NASHRI- CHANANI	5/2011	6/2015 (-) [0/0]	2,159.00 (2,519.00) [2,519.00]	4,705.68 (360.00) [0]
453	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	7/2010	7/2015 (12/2019) [9/2020]	1,987.00 (-) [1,987.00]	2,700.65 (0.00) [62]
454	SRINAGAR TO BANIHAL	6/2011	6/2014 (9/2017) [9/2020]	1,100.70 (-) [1,100.70]	2,880.38 (0.00) [75]
455	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA	3/2018	7/2019 (-) [0/0]	253.44 (-) [253.44]	0.00 (0.00) [0]
456	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0	3/2018	8/2018 (-) [0/0]	404.17 (-) [404.17]	90.94 (0.00) [0]
457	WIDENING AND UPGADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM	3/2018	11/2018 (-) [0/0]	216.00 (-) [216.00]	33.11 (0.00) [0]
	<u>JHARKHAND</u>				
	<u>Coal</u>				
458	AMRAPALI OC(12MTY)	2/2012	3/2020	858.11	194.12

			(-) [3/2020]	(-) [858.11]	(0.00) [0]
459	CHITRA EAST (RCE) OCP	8/2018	3/2024 (-) [3/2024]	513.98 (-) [513.98]	90.23 (0.00) [0]
460	CHURI BENTI UG (0.81 MTY)	8/2007	3/2011 (-) [3/2021]	163.51 (-) [163.51]	106.41 (0.00) [120]
461	HURA - C OC (3 MTY)	10/2015	3/2022 (-) [3/2022]	359.69 (-) [359.69]	83.23 (0.00) [0]
462	KAPURIA UG(PSLW)	8/2011	4/2017 (-) [0/0]	988.35 (-) [988.35]	45.26 (0.00) [0]
463	KARMA OCP (1.0MTY)	6/2009	3/2014 (-) [3/2021]	162.46 (-) [162.46]	90.78 (0.00) [84]
464	MADHUBAND NLW WASHERY	8/2010	5/2014 (-) [3/2020]	289.45 (-) [289.45]	257.56 (0.00) [70]
465	MAGADH OC 20 MTY (CCL)	8/2008	7/2012 (-) [3/2022]	706.40 (-) [706.40]	354.93 (0.00) [116]
466	MOONIDIH XV SEAM UG	8/2011	4/2015 (-) [0/0]	1,230.27 (-) [1,230.27]	394.32 (0.00) [0]
467	MURAI DIH UG TURN-KEY PROJECT	2/2011	4/2014 (-) [0/0]	339.88 (-) [339.88]	12.08 (0.00) [0]
468	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY)	2/2014	3/2021 (-) [3/2021]	555.52 (-) [555.52]	5.24 (0.00) [0]
469	NORTH URIMARI EXPANSION OCP	3/2019	3/2023 (-) [3/2023]	1,553.06 (-) [1,553.06]	163.23 (0.00) [0]
470	PATHERDIH NLW WASHERY	10/2012	4/2014 (-) [11/2019]	269.82 (-) [269.82]	180.83 (0.00) [67]
471	RAJRAPPA RCE OCP (3.0 MTY)	12/2009	3/2016 (-) [3/2021]	510.85 (-) [510.85]	362.49 (0.00) [60]
472	TAPIN OCP (2.5 MTY)	8/2008	3/2012 (-) [3/2021]	264.68 (-) [264.68]	181.17 (0.00) [108]
	<u>Petroleum</u>				
473	120 TMTPA NEW LPG PLANT AT BARHI JHARKAND STATE	6/2017	6/2020 (-) [9/2021]	161.50 (-) [161.50]	17.78 (0.00) [15]
474	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR	10/2017	10/2022 (-) [10/2022]	221.45 (-) [221.45]	46.15 (0.00) [0]
475	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI	10/2017	10/2022 (-) [10/2022]	226.45 (-) [226.45]	50.15 (0.00) [0]
476	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	12/2015	3/2023 (3/2022) [3/2022]	823.27 (910.23) [910.23]	356.00 (86.96) [-12]
477	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO.	11/2018	6/2022 (-) [6/2022]	248.55 (-) [248.55]	22.86 (0.00) [0]
	<u>Power</u>				

478	NORTH KARANPURA STPP (3X660 MW)	2/2014	6/2019 (9/2019) [9/2021]	14,366.58 (-) [15,164.05]	9,221.99 (797.47) [27]
479	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017 (-) [0/0]	4,237.96 (4,238.00) [4,552.00]	3,268.00 (314.04) [0]
480	PATRATU STPP-I (3X800MW)	11/2017	3/2023 (-) [3/2023]	18,668.00 (-) [18,668.00]	2,004.32 (0.00) [0]
	<u>Railways</u>				
481	BONDAMUNDA RANCHI DOUBLING	3/2016	3/2021 (-) [12/2021]	1,724.20 (-) [1,993.24]	384.82 (269.04) [9]
482	GARHWA ROAD-RAMNA	3/2015	3/2021 (-) [12/2020]	348.23 (-) [348.23]	177.12 (0.00) [-3]
483	KODERMA-RANCHI VIA BARKAKANA (NL), ECR	3/1999	/ (-) [3/2021]	1,033.07 (3,020.95) [3,376.00]	3,307.82 (2,342.93) [-]
484	KODERMA-TILAIYA (NL), ECR	4/2002	/ (-) [3/2021]	459.91 (1,625.87) [1,625.87]	508.33 (1,165.96) [-]
485	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	4/2012	12/2018 (12/2018) [6/2020]	258.20 (358.68) [358.68]	258.09 (100.48) [18]
486	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	4/2012	12/2016 (8/2018) [12/2019]	148.77 (-) [377.00]	180.95 (228.23) [36]
	<u>Road Transport And Highways</u>				
487	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00)	3/2017	3/2020 (-) [3/2020]	239.68 (-) [235.90]	91.24 (-3.78) [0]
488	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00)	3/2017	3/2020 (-) [9/2019]	165.50 (-) [172.16]	117.09 (6.66) [-6]
489	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K	3/2018	/ (3/2019) [3/2021]	1,005.08 (1,073.10) [1,005.08]	0.00 (0.00) [-]
490	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION	2/2016	3/2019 (-) [7/2019]	997.15 (-) [997.15]	728.62 (0.00) [0]
491	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31	1/2018	/ (-) [0/0]	273.46 (-) [273.46]	0.00 (0.00) [0]
492	FOUR LANING OF BARHI-HAZARIBAGH NH-33	8/2016	8/2018 (-) [1/2020]	323.72 (-) [323.72]	252.99 (0.00) [17]
493	RANCHI-RARGA-JAMSETHPUR	12/2012	6/2015 (-) [0/0]	1,479.00 (-) [1,479.00]	740.26 (0.00) [0]
494	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L	3/2018	6/2020 (-) [6/2020]	212.99 (-) [212.99]	80.47 (0.00) [0]
495	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION	1/2018	/ (-) [0/0]	1,155.16 (-) [1,155.16]	0.00 (0.00) [0]
496	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH-	7/2016	/ (12/2017) [12/2019]	458.03 (-) [458.03]	303.12 (0.00) [-]
	<u>Steel</u>				
497	MODERNISATION OF STEEL MELTING SHOP NO.1 AT	5/2015	12/2017	1,154.18	963.95

	BOKARO STEEL PLANT		(11/2019) [11/2019]	(-) [1,154.18]	(0.00) [23]
498	NEW SINTER PLANT AT BOKARO STEEL PLANT	3/2015	10/2017 (6/2020) [6/2020]	1,034.01 (-) [1,034.01]	436.08 (0.00) [32]
499	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	11/2016	6/2019 (6/2020) [6/2020]	262.87 (-) [262.87]	104.85 (0.00) [12]
	<u>Urban Development</u>				
500	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	9/2012	3/2016 (-) [9/2020]	171.86 (-) [171.86]	85.33 (0.00) [54]
501	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT	12/2007	3/2018 (-) [0/0]	200.00 (-) [200.00]	131.15 (0.00) [0]
502	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY	4/2013	4/2018 (-) [0/0]	170.00 (-) [170.00]	88.91 (0.00) [0]
503	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII	2/2014	12/2016 (-) [0/0]	787.29 (-) [787.29]	285.30 (0.00) [0]
504	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY-JHARKHAND	12/2007	6/2016 (-) [0/0]	253.92 (253.92) [253.92]	193.97 (0.00) [0]
	<u>KARNATAKA</u>				
	<u>Petroleum</u>				
505	BSVI UPGRADATION	9/2016	12/2019 (7/2020) [7/2020]	1,810.00 (1,810.00) [1,810.00]	823.40 (0.00) [7]
506	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU	5/2015	4/2019 (-) [0/0]	224.00 (207.00) [185.00]	164.61 (-39.00) [0]
507	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE	12/2018	12/2022 (-) [12/2022]	854.00 (-) [854.00]	38.34 (0.00) [0]
508	GAIL GAS LTD BENGALURU CGD PROJECT	2/2015	2/2020 (-) [2/2020]	749.00 (-) [842.00]	606.89 (93.00) [0]
509	HASSAN CHERLAPALLI LPG PIPELINE	6/2019	6/2022 (-) [6/2022]	2,166.38 (-) [2,166.38]	9.80 (0.00) [0]
510	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE	10/2015	3/2019 (10/2019) [10/2019]	135.00 (170.70) [170.70]	156.65 (35.70) [7]
511	RESITEMENT OF RAICHUR DEPOT TO GULBARGA	10/2018	3/2021 (-) [3/2021]	206.26 (-) [206.26]	0.98 (0.00) [0]
512	SEA WATER DESALINATION PLANT	11/2017	3/2020 (-) [9/2020]	581.00 (-) [621.00]	84.47 (40.00) [6]
513	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	1/2006	1/2012 (-) [0/0]	993.00 (-) [1,693.00]	1,549.85 (700.00) [0]
	<u>Power</u>				
514	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B)	5/2017	2/2019 (-) [3/2020]	445.89 (-) [445.89]	285.22 (0.00) [13]
	<u>Railways</u>				
515	ARSIKERE-TUMKUR	3/2015	3/2020 (-) [3/2020]	578.00 (-) [578.00]	509.07 (0.00) [0]

516	BAGALKOT-KUDACHI NL	4/2010	3/2016 (-) [12/2023]	986.30 (-) [986.30]	297.70 (0.00) [93]
517	BANGLORE - SATYAMANGALAM (NL)(SWR)	4/1996	3/2002 (-) [3/2024]	1,382.78 (-) [1,382.78]	7.35 (0.00) [264]
518	CHIKBALLA-PUR-GOWRIBIDANUR NL	4/2013	/ (-) [12/2023]	327.25 (-) [367.77]	0.00 (40.52) [-]
519	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	4/2013	/ (-) [12/2023]	558.00 (-) [692.43]	0.00 (134.43) [-]
520	GADAG-WADI NL	4/2013	12/2018 (-) [12/2024]	2,841.84 (-) [2,841.84]	113.63 (0.00) [72]
521	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	4/2010	3/2023 (-) [3/2024]	2,127.00 (-) [2,900.00]	1,660.87 (773.00) [12]
522	HUBLI- CHIKJAJUR	3/2015	3/2020 (-) [3/2021]	1,156.94 (-) [1,140.93]	786.13 (-16.01) [12]
523	HUBLI-ANKOLA(NL),SWR	4/1997	/ (-) [12/2024]	2,315.00 (-) [2,135.00]	144.76 (-180.00) [-]
524	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	3/1996	3/2017 (-) [3/2020]	644.78 (-) [889.52]	438.39 (244.74) [36]
525	MARIKUPPAM - KUPPAM	4/2012	3/2016 (-) [12/2023]	279.54 (-) [279.54]	28.51 (0.00) [93]
526	SHIMOGA-HARIHAR NL	4/2011	3/2016 (-) [3/2024]	832.47 (-) [832.47]	0.94 (0.00) [96]
527	TORANAGALLU-RANJITPURA DL	4/2011	/ (-) [12/2023]	146.75 (-) [167.50]	0.34 (20.75) [-]
528	TUMKUR-CHITRADURGA-DAVENGERE NL	4/2011	/ (-) [12/2023]	1,801.01 (-) [1,801.01]	44.36 (0.00) [-]
529	WHITE FIELD-KOLAR NL	4/2011	/ (-) [12/2023]	348.85 (-) [348.85]	0.35 (0.00) [-]
	<u>Road Transport And Highways</u>				
530	HOSPET-BELLARY-KARNATAKA AP BORDER	8/2016	3/2019 (3/2017) [8/2020]	1,167.42 (870.00) [870.00]	254.96 (-297.42) [17]
531	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM	2/2018	/ (-) [0/0]	486.78 (-) [486.78]	113.59 (0.00) [0]
532	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	5/2014	8/2016 (-) [12/2020]	1,655.01 (-) [1,655.01]	1,867.51 (0.00) [52]
533	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	3/2016	3/2019 (-) [11/2020]	701.40 (-) [701.40]	29.48 (0.00) [20]
534	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL	3/2016	3/2019 (-) [11/2020]	870.00 (-) [870.00]	36.30 (0.00) [20]
535	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION	2/2017	5/2019 (-) [5/2021]	157.32 (188.00) [157.32]	0.00 (0.00) [24]

536	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT	5/2018	5/2018 (-) [5/2020]	171.60 (-) [171.60]	0.86 (0.00) [24]
537	FOUR LANING OF HOSPET - CHITRADURGA	3/2015	8/2018 (-) [3/2020]	1,388.00 (-) [1,388.00]	1,153.07 (0.00) [19]
538	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB	8/2016	4/2020 (-) [4/2020]	1,664.20 (-) [1,664.20]	657.08 (0.00) [0]
539	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	9/2010	6/2018 (-) [12/2019]	946.00 (-) [946.00]	818.53 (0.00) [18]
540	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN	3/2018	10/2018 (-) [0/0]	325.86 (-) [325.86]	62.54 (0.00) [0]
541	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH	8/2016	2/2017 (-) [0/0]	175.50 (-) [175.50]	86.54 (0.00) [0]
542	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2	3/2018	6/2019 (-) [0/0]	159.97 (-) [159.97]	0.00 (0.00) [0]
543	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM.	1/2014	8/2014 (-) [0/0]	471.16 (-) [471.16]	128.32 (0.00) [0]
544	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	1/1991	1/2018 (-) [0/0]	219.40 (-) [219.40]	0.00 (0.00) [0]
545	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O	3/2017	3/2020 (-) [6/2020]	993.16 (-) [1,434.00]	645.75 (440.84) [3]
546	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	3/2017	3/2020 (-) [7/2020]	831.58 (-) [1,177.00]	586.20 (345.42) [4]
547	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA	2/2018	/ (10/2019) [0/0]	2,177.80 (2,283.50) [2,450.00]	793.30 (272.20) [0]
548	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT	2/2018	/ (5/2019) [11/2021]	1,995.34 (2,190.00) [2,400.00]	1,555.77 (404.66) [-]
549	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP	3/2015	11/2015 (-) [0/0]	165.67 (-) [165.67]	0.00 (0.00) [0]
550	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU	3/2015	11/2015 (-) [0/0]	159.12 (-) [159.12]	0.00 (0.00) [0]
551	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	9/2016	8/2019 (-) [12/2020]	950.69 (1,008.00) [1,108.00]	1,354.09 (157.31) [16]
552	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN	10/2016	3/2017 (-) [0/0]	396.96 (-) [396.96]	113.98 (0.00) [0]
553	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT	11/2016	3/2017 (-) [0/0]	314.90 (-) [314.90]	104.40 (0.00) [0]
554	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT	8/2016	1/2017 (-) [0/0]	367.44 (-) [367.44]	61.95 (0.00) [0]
555	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT	8/2016	2/2017 (-) [0/0]	329.01 (-) [329.01]	135.50 (0.00) [0]
556	WIDENING TO TWO LANE WITH PAVED SHOULDER	9/2017	10/2018	191.60	26.24

	FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR		(-) [0/0]	(-) [191.60]	(0.00) [0]
557	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U	1/2017	8/2017 (-) [0/0]	291.49 (-) [291.49]	130.00 (0.00) [0]
558	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA	1/2017	9/2017 (-) [0/0]	166.67 (-) [166.67]	117.05 (0.00) [0]
559	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT	8/2016	1/2017 (-) [0/0]	175.20 (-) [175.20]	113.38 (0.00) [0]
560	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH-	12/2017	1/2019 (-) [0/0]	297.30 (-) [297.30]	0.00 (0.00) [0]
561	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION	1/2018	7/2018 (-) [0/0]	159.70 (-) [159.70]	22.79 (0.00) [0]
562	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776)	3/2015	1/2016 (-) [0/0]	165.67 (-) [165.67]	87.63 (0.00) [0]
563	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775)	3/2015	1/2016 (-) [0/0]	159.12 (-) [159.12]	96.22 (0.00) [0]
	<u>Urban Development</u>				
564	BANGALORE METRO RAIL PROJECT PHASE-2	2/2014	2/2019 (-) [3/2020]	26,405.14 (-) [26,405.14]	499.85 (0.00) [13]
565	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	5/2005	2/2014 (-) [0/0]	768.88 (1,070.97) [1,113.34]	1,085.64 (344.46) [0]
566	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA	7/2011	12/2015 (-) [0/0]	324.87 (324.87) [324.87]	262.93 (0.00) [0]
567	RESIDENTIAL QUATERS FOR HAL,BANGLORE	12/2016	2/2020 (-) [9/2020]	246.31 (-) [246.31]	72.38 (0.00) [7]
	<u>KERALA</u>				
	<u>Petroleum</u>				
568	KOCHI SALEM LPG PIPELINE PROJECT	12/2015	6/2019 (2/2022) [2/2022]	1,112.00 (1,507.24) [1,507.24]	525.00 (395.24) [32]
569	LPG TERMINAL AT KOCHI	10/2015	10/2017 (-) [0/0]	607.06 (-) [714.25]	355.48 (107.19) [0]
570	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY	2/2016	2/2020 (10/2020) [10/2020]	3,313.00 (3,288.96) [3,288.96]	1,151.10 (-24.04) [8]
571	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	11/2014	8/2018 (11/2019) [11/2019]	4,588.29 (5,245.96) [5,245.96]	3,711.38 (657.67) [15]
572	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC	9/2018	3/2023 (-) [3/2023]	11,130.00 (-) [11,130.00]	18.14 (0.00) [0]
	<u>Railways</u>				
573	ANGAMALI-SABARIMALA (N.L.)(SR)	10/1998	/ (-) [0/0]	1,566.00 (2,815.62) [2,815.62]	264.28 (1,249.62) [0]
574	ERNAKULAM-KUMBALAM	4/2010	/ (-) [0/0]	189.24 (189.24) [189.24]	6.72 (0.00) [0]
575	KUMBALAM-TURAVUR	4/2011	/	252.96	8.50

			(-) [0/0]	(252.96) [252.96]	(0.00) [0]
576	PALAKKAD - SETTING UP OF RAIL COACH FACTORY	2/2012	3/2016 (-) [0/0]	550.00 (-) [550.00]	0.00 (0.00) [0]
577	TRIVANDRUM-KANYAKUMARI DOUBLING	2/2015	/ (6/2022) [0/0]	1,431.90 (1,431.90) [1,431.90]	75.00 (0.00) [0]
578	TURAVUR-AMBALAPUZHA DOUBLING	2/2015	/ (-) [0/0]	1,000.00 (828.50) [828.50]	0.08 (-171.50) [0]
Road Transport And Highways					
579	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47	6/2015	/ (-) [10/2019]	845.24 (-) [941.00]	824.26 (95.76) [-]
580	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T	4/2016	6/2018 (-) [4/2020]	804.97 (-) [804.97]	438.27 (0.00) [22]
581	4-LANNING OF THALSERRY -MAHE BYPASS	9/2017	9/2017 (-) [6/2020]	1,124.11 (-) [1,232.76]	278.60 (108.65) [33]
582	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH	2/2018	/ (-) [0/0]	1,424.77 (-) [1,853.42]	14.19 (428.65) [0]
583	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1	1/2014	9/2017 (-) [12/2019]	255.75 (348.00) [348.43]	290.12 (92.68) [27]
584	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM	2/2010	8/2012 (-) [12/2019]	617.00 (-) [617.00]	943.17 (0.00) [88]
Urban Development					
585	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST	9/2017	3/2020 (-) [3/2020]	150.29 (-) [150.29]	2.58 (0.00) [0]
586	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	1/2010	10/2012 (-) [3/2020]	165.23 (-) [165.23]	92.05 (0.00) [89]
587	KOCHI METRO RAIL PROJECT	7/2012	7/2017 (-) [12/2019]	5,181.79 (-) [5,687.79]	5,188.00 (506.00) [29]
MADHYA PRADESH					
Coal					
588	AMADAND OPENCASE EXPANSION PROJECT	3/2016	3/2021 (-) [3/2021]	869.44 (-) [869.44]	116.48 (0.00) [0]
589	AMRITHARA OC PROJECT	2/2015	3/2023 (-) [3/2023]	481.60 (-) [481.60]	0.00 (0.00) [0]
590	BATURA HIGHWALL PROJECT	7/2015	3/2022 (-) [3/2022]	231.92 (-) [231.92]	0.00 (0.00) [0]
591	BATURA OCP (2.0 MTY)	8/2015	3/2023 (-) [3/2021]	1,186.64 (-) [203.82]	121.39 (-982.82) [-24]
592	BLOCK-B EXPANSION OPENCASE PROJECT	7/2019	3/2023 (-) [3/2023]	998.71 (-) [998.71]	0.00 (0.00) [0]
593	COAL PROJECT NAME JAMUNIA UG (0.84 MTY)	7/2016	3/2022 (-) [3/2022]	409.87 (-) [409.87]	20.30 (0.00) [0]
594	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA)	11/2017	3/2022	1,255.17	95.24

			(-) [3/2022]	(-) [1,255.17]	(0.00) [0]
595	GANDHIGRAM UG MINE	8/2019	3/2026 (-) [3/2026]	414.16 (-) [414.16]	0.00 (0.00) [0]
596	JAYANT EXPANSION OCP 10 TO 20 MTPA	5/2017	3/2021 (-) [3/2021]	1,783.09 (-) [1,783.09]	267.80 (0.00) [0]
597	KANCHAN OC EXPANSION	12/2014	3/2021 (-) [3/2021]	371.04 (-) [371.04]	52.43 (0.00) [0]
598	MALACHUA OPENCAST PROJECT	10/2015	3/2023 (-) [3/2023]	488.33 (-) [488.33]	27.10 (0.00) [0]
599	RAJNAGAR OCP RPR (1.70 MTY)	12/2014	3/2021 (-) [3/2021]	357.80 (-) [357.80]	104.06 (0.00) [0]
600	SEMARIA OPENCAST PROJECT	5/2019	3/2026 (-) [3/2026]	396.58 (-) [396.58]	0.00 (0.00) [0]
601	VISHNUPURI UG TO OC MINE	7/2018	3/2025 (-) [3/2025]	195.57 (-) [195.57]	2.94 (0.00) [0]
	<u>Petroleum</u>				
602	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND	8/2017	6/2020 (-) [8/2020]	236.00 (-) [236.00]	24.15 (0.00) [2]
	<u>Power</u>				
603	AMELIA COAL MINE	1/2017	9/2020 (-) [9/2020]	2,104.21 (-) [1,587.16]	307.48 (-517.05) [0]
604	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	3/2013	1/2018 (3/2020) [3/2020]	11,638.55 (-) [12,865.92]	12,188.01 (1,227.37) [26]
605	KHARGONE STPP STAGE I (1320 MW)	3/2015	1/2020 (-) [1/2020]	9,870.51 (-) [11,148.86]	8,619.60 (1,278.35) [0]
	<u>Railways</u>				
606	ANUPPUR-KATNI	4/2015	12/2021 (12/2021) [12/2021]	1,370.00 (1,370.00) [1,370.00]	281.19 (0.00) [0]
607	BINA - KOTA DOUBLING WITH RE	4/2011	12/2020 (-) [3/2021]	1,485.85 (-) [1,485.85]	1,074.88 (0.00) [3]
608	CHHINDWARA - NAGPUR (GC)(SECR)	4/2005	/ (-) [10/2019]	383.79 (-) [1,413.76]	1,324.64 (1,029.97) [-]
609	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	4/2010	2/2019 (3/2020) [6/2020]	585.93 (737.72) [1,300.44]	646.30 (714.51) [16]
610	INDORE-DEWAS-UJJAIN (80 KMS)	4/2016	6/2020 (6/2021) [6/2021]	700.00 (603.69) [603.69]	92.30 (-96.31) [12]
611	KATNI - SINGRAULI DOUBLING PROJECT	12/2015	3/2020 (-) [3/2022]	1,763.93 (-) [1,763.93]	624.49 (0.00) [24]
612	KATNI GRADE SEPARATOR/BYE PASS	8/2016	3/2022 (-) [9/2022]	582.13 (-) [1,247.64]	154.63 (665.51) [6]
613	KATNI-BINA 3RD LINE (263 KM)	6/2016	3/2022 (-)	2,478.23 (-)	367.59 (0.00)

			[3/2023]	[2,478.23]	[12]
614	MULTI MODAL LOGISTICS PARK AT TIHI	12/2015	3/2019 (-) [2/2020]	174.00 (-) [174.00]	151.24 (0.00) [11]
615	RAMGANJMUUNDI-BHOPAL (NL),WCR	4/2001	3/2021 (-) [3/2023]	424.60 (-) [2,909.99]	1,926.25 (2,485.39) [24]
616	RATLAM-MHOW-KHANDWA-AKOLA (GC)	4/2008	3/2022 (3/2023) [3/2023]	3,503.69 (3,860.00) [3,860.40]	1,676.43 (356.71) [12]
	<u>Road Transport And Highways</u>				
617	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP	3/2018	11/2019 (-) [11/2019]	191.21 (-) [191.21]	72.02 (0.00) [0]
618	2L+PS OF THIKRI ANJAD SECTION OF NH-347B	11/2017	7/2018 (-) [1/2020]	249.05 (-) [249.05]	118.29 (0.00) [18]
619	ANJANGAON TO MAH/MP BORDER	1/2017	6/2019 (-) [0/0]	359.00 (359.00) [359.00]	182.80 (0.00) [0]
620	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN	12/2017	/ (-) [0/0]	950.27 (-) [950.27]	0.00 (0.00) [0]
621	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM.	11/2017	3/2018 (-) [11/2019]	392.33 (-) [392.33]	242.88 (0.00) [20]
622	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION	8/2016	1/2019 (-) [8/2019]	227.49 (-) [227.49]	140.57 (0.00) [0]
623	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12	9/2017	9/2017 (-) [0/0]	374.40 (-) [374.40]	0.00 (0.00) [0]
624	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69	9/2017	9/2017 (-) [1/2021]	990.61 (-) [990.61]	17.41 (0.00) [40]
625	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP	8/2015	/ (-) [0/0]	257.80 (-) [257.00]	12.38 (-0.80) [0]
626	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A	6/2015	/ (-) [3/2020]	390.51 (-) [390.51]	191.77 (0.00) [-]
627	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA	10/2019	/ (-) [0/0]	743.88 (-) [743.88]	0.00 (0.00) [0]
628	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH.	1/2017	3/2017 (-) [6/2020]	205.05 (-) [205.05]	73.22 (0.00) [39]
629	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD	1/2019	3/2021 (-) [3/2021]	264.50 (-) [264.50]	0.00 (0.00) [0]
630	FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR	6/2015	1/2019 (-) [0/0]	1,583.79 (-) [1,583.79]	1,568.11 (0.00) [0]
631	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO	1/2018	/ (-) [8/2020]	960.24 (-) [960.24]	328.34 (0.00) [-]
632	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA	6/2015	3/2016 (-) [0/0]	1,012.90 (-) [1,012.90]	226.10 (0.00) [0]
633	FOUR LANING OF GWALIOR-SHIVPURI	5/2013	11/2015 (-)	1,055.00 (-)	1,393.40 (546.77)

			[0/0]	[1,601.77]	[0]
634	FOUR LANING OF JABALPUR - LAKHNADON	3/2015	/ (6/2015) [6/2015]	928.83 (-) [928.83]	593.31 (0.00) [0]
635	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I	3/2015	/ (-) [10/2019]	794.30 (622.00) [622.00]	582.73 (-172.30) [-]
636	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II	3/2015	/ (-) [10/2019]	795.76 (622.00) [622.00]	629.18 (-173.76) [-]
637	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV	3/2015	/ (6/2015) [6/2015]	810.22 (-) [810.22]	664.56 (0.00) [0]
638	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124.	10/2017	10/2017 (-) [1/2020]	639.97 (-) [639.97]	274.24 (0.00) [27]
639	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER	1/2018	/ (-) [0/0]	770.73 (-) [770.73]	0.00 (0.00) [0]
640	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93	12/2015	2/2020 (-) [2/2020]	957.54 (-) [957.54]	467.50 (0.00) [0]
641	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	11/2013	5/2017 (-) [5/2020]	497.05 (-) [881.05]	544.84 (384.00) [36]
642	INDORE-DEWAS(NH-3)	11/2010	5/2013 (-) [0/0]	325.00 (-) [325.00]	469.54 (0.00) [0]
643	INDORE-JHABUA-GUJRAT/MP	10/2010	4/2013 (-) [0/0]	1,175.00 (-) [1,175.00]	1,342.77 (0.00) [0]
644	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400	11/2015	1/2020 (-) [1/2020]	628.45 (-) [628.45]	252.21 (0.00) [0]
645	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP	1/2012	4/2015 (-) [10/2019]	410.72 (-) [410.72]	216.14 (0.00) [54]
646	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA	2/2018	3/2018 (-) [7/2020]	169.63 (-) [169.63]	9.35 (0.00) [28]
647	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86	9/2016	9/2018 (-) [8/2019]	178.23 (-) [178.23]	114.16 (0.00) [0]
648	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175	9/2016	1/2019 (-) [11/2019]	287.34 (-) [287.34]	148.65 (0.00) [10]
649	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM	3/2016	6/2019 (-) [11/2019]	877.79 (-) [877.79]	436.12 (0.00) [5]
650	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID	11/2017	2/2018 (-) [11/2019]	235.91 (-) [235.91]	117.24 (0.00) [21]
651	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS	1/2016	7/2018 (-) [2/2020]	809.16 (-) [809.16]	219.42 (0.00) [19]
652	SATANA-BELA SECTION OF NH-75(4L) IN MP	1/2012	8/2015 (-) [0/0]	320.48 (-) [320.48]	189.49 (0.00) [0]
653	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	11/2011	9/2015 (-) [3/2020]	954.43 (-) [954.43]	235.61 (0.00) [54]

654	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200	3/2015	8/2017 (-) [2/2020]	511.83 (-) [511.83]	240.05 (0.00) [30]
655	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS	11/2017	2/2018 (-) [11/2019]	254.17 (-) [254.17]	139.86 (0.00) [21]
656	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS	3/2018	3/2018 (-) [11/2019]	233.04 (-) [233.04]	95.28 (0.00) [20]
657	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS	2/2018	3/2018 (-) [4/2020]	279.44 (-) [279.44]	76.00 (0.00) [25]
658	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS	3/2018	8/2018 (-) [6/2020]	166.21 (-) [166.21]	30.52 (0.00) [22]
659	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS	11/2017	2/2018 (-) [11/2019]	184.62 (-) [184.62]	55.27 (0.00) [21]
660	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS	3/2018	3/2018 (-) [11/2019]	214.69 (-) [214.69]	23.06 (0.00) [20]
661	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS	3/2018	8/2018 (-) [6/2020]	217.22 (-) [217.22]	20.43 (0.00) [22]
662	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS	3/2018	3/2018 (-) [12/2019]	162.56 (-) [162.56]	88.47 (0.00) [21]
663	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A	1/2017	9/2019 (-) [5/2020]	373.82 (-) [373.82]	116.34 (0.00) [8]
	<u>Urban Development</u>				
664	BHOPAL METRO RAIL	11/2018	2/2023 (-) [2/2023]	6,941.40 (-) [6,941.40]	34.12 (0.00) [0]
665	INDORE METRO RAIL	11/2018	2/2023 (-) [2/2023]	7,500.80 (-) [7,500.80]	42.62 (0.00) [0]
	<u>MAHARASHTRA</u>				
	<u>Civil Aviation</u>				
666	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT	3/2017	4/2021 (-) [4/2021]	358.89 (-) [358.89]	29.73 (0.00) [0]
	<u>Coal</u>				
667	ADASA UG TO OC	8/2015	3/2023 (-) [3/2024]	288.90 (-) [333.43]	21.02 (44.53) [12]
668	AMALGAMATED GONDEGAON GHATROHAN OC	2/2016	3/2019 (-) [0/0]	198.68 (-) [198.68]	184.77 (0.00) [0]
669	AMALGAMATED PAUNI-II III OC MINE	6/2015	3/2021 (-) [3/2021]	483.69 (-) [483.69]	210.32 (0.00) [0]
670	AMALGAMATED YEKONA-I YEKONA-II	8/2015	3/2025 (-) [3/2025]	727.28 (-) [727.28]	268.58 (0.00) [0]
671	BELLORA-NAIGAON DEEP OC	11/2018	3/2021 (-) [3/2021]	252.71 (-) [252.71]	44.94 (0.00) [0]
672	BHANEGAON OC	2/2015	3/2023 (-) [3/2023]	187.94 (-) [409.68]	128.90 (221.74) [0]

673	BHATADI EXPANSION OC MINE	2/2016	3/2019 (-) [0/0]	304.52 (-) [304.52]	153.29 (0.00) [0]
674	DINESH OCP	11/2014	3/2020 (-) [3/2020]	611.16 (-) [611.16]	413.13 (0.00) [0]
675	GAURI DEEP OC	10/2016	3/2019 (-) [0/0]	164.96 (-) [164.96]	93.37 (0.00) [0]
676	KAMPTEE DEEP OC MINE	11/2015	3/2021 (-) [3/2024]	277.65 (-) [313.34]	116.34 (35.69) [36]
677	KOLAR PIMPRI EXTENSION OC	3/2017	3/2020 (-) [3/2020]	362.73 (-) [362.73]	319.93 (0.00) [0]
678	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE	11/2015	3/2020 (-) [3/2020]	498.42 (-) [498.42]	182.76 (0.00) [0]
679	NEW MAJRI UG TO OC	5/2015	3/2019 (-) [0/0]	295.56 (-) [295.56]	123.60 (0.00) [0]
680	PENGANGA OCP(REVISED)	9/2014	3/2020 (-) [3/2020]	441.82 (-) [441.82]	213.24 (0.00) [0]
681	SAONER I UG TO OC PHASE I	11/2016	3/2022 (-) [3/2022]	162.10 (-) [162.10]	50.56 (0.00) [0]
682	SINGHORI OC MINE	6/2015	3/2020 (-) [3/2020]	205.49 (-) [205.49]	121.74 (0.00) [0]
683	UKNI DEEP OC	11/2018	3/2021 (-) [3/2021]	318.14 (-) [318.14]	146.45 (0.00) [0]
	<u>Fertilisers</u>				
684	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY	4/2018	4/2020 (-) [4/2020]	426.72 (-) [426.72]	197.47 (0.00) [0]
685	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	11/2016 (-) [9/2019]	197.79 (-) [209.44]	174.52 (11.65) [34]
	<u>Health And Family Welfare</u>				
686	HOSPITAL AND TEACHING- AIIMS NAGPUR	3/2018	/ (-) [2/2020]	582.99 (-) [582.99]	112.97 (0.00) [-]
687	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA	8/2017	3/2019 (-) [10/2019]	274.19 (-) [274.19]	169.93 (0.00) [7]
	<u>Information And Broadcasting</u>				
688	NATIONAL CENTRE OF EXCELLENCE FOR ANIMATION VISUAL EFFECTS GAMING AND COMICS	12/2016	3/2020 (-) [3/2020]	167.70 (-) [167.70]	0.00 (0.00) [0]
689	NATIONAL FILM HERITAGE MISSION	11/2014	/ (-) [0/0]	597.41 (-) [597.41]	29.80 (0.00) [0]
	<u>Petroleum</u>				
690	180 TMTPA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA	6/2017	6/2020 (-) [9/2021]	249.26 (-) [249.26]	60.45 (0.00) [15]
691	4TH PHASE DEVELOPMENT OF NBP FIELD	2/2017	11/2019 (-) [11/2019]	968.61 (-) [1,033.95]	930.62 (65.34) [0]

692	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELI	5/2016	1/2021 (-) [1/2021]	261.00 (-) [261.00]	41.42 (0.00) [0]
693	ADDITIONAL FACILITIES AT MANMAD FOR COVERION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [4/2021]	212.00 (-) [212.00]	38.55 (0.00) [3]
694	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [10/2021]	348.00 (-) [348.00]	30.75 (0.00) [9]
695	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	3/2011	5/2013 (12/2019) [12/2019]	861.79 (-) [1,683.06]	1,322.31 (821.27) [79]
696	DEVELOPMENT OF B-147 FIELD	2/2017	11/2019 (3/2020) [3/2020]	546.15 (565.15) [565.15]	442.18 (19.00) [4]
697	DEVELOPMENT OF BSE-11 BLOCK	2/2017	11/2019 (-) [11/2019]	511.30 (-) [511.30]	476.47 (0.00) [0]
698	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION	2/2019	5/2021 (-) [5/2021]	2,292.46 (-) [2,292.46]	300.13 (0.00) [0]
699	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)	2/2017	5/2021 (12/2021) [12/2021]	4,006.83 (-) [4,475.92]	2,796.50 (469.09) [7]
700	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA	1/2015	12/2017 (3/2020) [3/2020]	4,619.94 (-) [4,619.94]	4,360.59 (0.00) [27]
701	HEERA REDEVELOPMENT - PHASE III	5/2019	12/2021 (-) [3/2022]	2,494.68 (-) [2,494.68]	0.00 (0.00) [3]
702	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY	2/2016	2/2020 (-) [10/2019]	554.00 (-) [554.00]	363.86 (0.00) [-4]
703	INTEGRATED DEVELOPMENT OF B-127 FIELDS	12/2011	3/2015 (12/2019) [12/2019]	2,059.63 (2,665.65) [2,665.65]	1,908.01 (606.02) [57]
704	KOYALI AHMEDNAGAR SOLAPUR PIPELINE	5/2016	8/2021 (-) [8/2021]	1,945.00 (-) [1,945.00]	960.09 (0.00) [0]
705	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	12/2015	4/2018 (5/2020) [5/2020]	3,190.69 (-) [3,247.19]	2,225.67 (56.50) [25]
706	MMPL PIPELINE REROUTING PROJECT	4/2013	12/2019 (-) [12/2019]	449.58 (-) [449.58]	155.32 (0.00) [0]
707	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	4/2019	3/2022 (-) [3/2022]	3,228.80 (-) [3,228.80]	458.52 (0.00) [0]
708	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III	11/2014	4/2019 (12/2019) [12/2019]	6,068.80 (-) [5,296.93]	4,758.62 (-771.87) [8]
709	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV	2/2019	4/2021 (-) [5/2021]	3,660.71 (3,740.05) [3,740.05]	126.66 (79.34) [1]
710	MUMBAI REFINERY EXPANSION PROJECT	9/2015	3/2020 (-) [3/2020]	4,199.00 (5,060.00) [5,060.00]	2,754.00 (861.00) [0]
711	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY	8/2015	3/2019 (5/2020) [5/2020]	2,818.88 (-) [2,818.88]	2,230.96 (0.00) [14]
712	PIPELINE REPLACEMENT PROJECT (PRP-VI)	5/2019	12/2020	763.92	0.00

			(-) [12/2020]	(-) [763.92]	(0.00) [0]
713	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE)	4/2018	12/2019 (-) [12/2019]	766.37 (-) [766.37]	449.88 (0.00) [0]
714	PUNE POL STORAGE DEPOT	8/2016	8/2020 (-) [8/2020]	282.64 (-) [282.64]	127.11 (0.00) [0]
	<u>Power</u>				
715	MOUDA STPP STAGE 2	3/2012	9/2016 (-) [0/0]	7,921.47 (-) [7,921.47]	5,302.00 (0.00) [0]
	<u>Railways</u>				
716	3RD LINE BETWEEN BHUSAWAL-JALGAON	4/2011	3/2019 (12/2019) [12/2019]	184.06 (199.12) [305.00]	269.39 (120.94) [9]
717	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	2/1997	3/2021 (-) [3/2022]	2,271.50 (-) [3,712.50]	2,380.30 (1,441.00) [12]
718	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	3/1996	3/2004 (-) [3/2021]	495.44 (1,781.98) [2,980.41]	1,417.63 (2,484.97) [204]
719	DAUND - MANMAD (236 KM)	2/2016	3/2023 (-) [3/2023]	1,876.00 (-) [2,081.27]	121.17 (205.27) [0]
720	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	3/2009	3/2020 (-) [3/2020]	713.48 (-) [1,950.00]	1,957.22 (1,236.52) [0]
721	DIGHI PORT NEW LINE	4/2015	12/2025 (-) [3/2025]	723.78 (-) [723.78]	0.19 (0.00) [-9]
722	INDORE - MANMAD VIA MALEGAON (368 KM)	2/2016	3/2024 (-) [3/2024]	9,968.00 (-) [9,968.00]	0.00 (0.00) [0]
723	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	2/2015	3/2023 (-) [3/2023]	2,449.91 (-) [2,449.91]	165.28 (0.00) [0]
724	KALYAN-KASARA 3RD LINE	4/2011	3/2021 (-) [3/2022]	792.89 (-) [1,377.48]	308.67 (584.59) [12]
725	MANMAD - JALGAON - 3RD LINE (160 KM)	2/2016	3/2022 (-) [3/2024]	1,035.16 (-) [1,035.16]	90.49 (0.00) [24]
726	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN	10/2013	3/2019 (-) [12/2019]	305.00 (-) [305.00]	261.28 (0.00) [9]
727	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM	3/2010	/ (-) [0/0]	265.88 (-) [265.88]	0.00 (0.00) [0]
728	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	4/2008	3/2014 (3/2021) [3/2021]	5,300.00 (918.53) [918.53]	284.75 (-4,381.47) [84]
729	PUNE-MIRAJ-LONDA (467 KM)	2/2015	3/2024 (-) [3/2022]	3,627.47 (3,627.00) [3,627.47]	686.42 (0.00) [-24]
730	PUNE-NASIK (265 KM)	2/2016	3/2024 (-) [3/2024]	2,425.00 (-) [5,341.68]	0.00 (2,916.68) [0]
731	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	9/2016	3/2023 (3/2023) [3/2023]	1,908.51 (2,686.63) [2,686.63]	443.56 (778.12) [0]

732	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE	4/2012	4/2016 (-) [0/0]	714.10 (-) [714.10]	65.20 (0.00) [0]
733	VAIBHAVWADI -KOLHAPUR (107 KM)	2/2016	3/2024 (-) [3/2024]	2,750.00 (-) [3,438.51]	0.00 (688.51) [0]
734	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A	3/2012	/ (-) [0/0]	217.38 (-) [217.38]	0.00 (0.00) [0]
735	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	6/2018	12/2021 (3/2023) [3/2023]	229.00 (403.00) [860.92]	39.69 (631.92) [15]
736	WARDHA - NAGPUR - 4TH LINE (76 KM)	2/2016	3/2023 (-) [3/2024]	637.95 (-) [637.95]	58.36 (0.00) [12]
737	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	2/2015	3/2022 (-) [3/2023]	1,272.19 (-) [1,272.19]	296.03 (0.00) [12]
738	WARDHA-NANDED MAHARASHTRA	4/2008	3/2023 (-) [3/2023]	3,168.29 (-) [3,168.29]	1,202.43 (0.00) [0]
739	WARDHA-SEWAGRAM NGP 3RD LINE	4/2012	3/2022 (-) [3/2024]	540.02 (-) [540.02]	235.70 (0.00) [24]
	<u>Road Transport And Highways</u>				
740	4 LANING OF AMRAVATI - CHIKHLI (PKG-I)	7/2015	5/2019 (-) [0/0]	2,288.18 (-) [2,288.18]	487.81 (0.00) [0]
741	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3)	7/2015	5/2019 (-) [0/0]	1,885.74 (-) [1,885.74]	1,636.02 (0.00) [0]
742	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	1/2015	7/2017 (-) [10/2019]	972.50 (-) [972.50]	1,492.00 (0.00) [27]
743	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104)	1/2018	/ (-) [8/2021]	607.00 (-) [607.00]	120.17 (0.00) [-]
744	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000)	1/2018	/ (10/2018) [4/2021]	621.00 (565.02) [621.00]	303.91 (0.00) [-]
745	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION	6/2014	11/2016 (-) [5/2020]	923.04 (-) [923.04]	755.97 (0.00) [42]
746	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	3/2017	3/2020 (-) [3/2020]	744.64 (-) [982.00]	0.00 (237.36) [0]
747	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700)	11/2016	/ (-) [7/2021]	1,071.61 (-) [1,071.61]	365.61 (0.00) [-]
748	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT	11/2016	3/2019 (-) [3/2021]	446.17 (-) [446.17]	38.97 (0.00) [24]
749	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575)	3/2017	3/2020 (-) [8/2020]	1,098.06 (-) [1,160.64]	1,082.97 (62.58) [5]
750	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE	3/2016	/ (-) [0/0]	1,142.62 (-) [1,142.62]	726.85 (0.00) [0]
751	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE	3/2016	/ (-) [0/0]	1,101.58 (-) [1,101.58]	0.00 (0.00) [0]

752	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI	11/2016	3/2019 (-) [2/2021]	400.25 (-) [400.25]	64.89 (0.00) [23]
753	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00)	11/2016	/ (-) [7/2021]	1,064.88 (-) [1,064.88]	0.00 (0.00) [-]
754	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580)	3/2017	3/2017 (5/2018) [11/2020]	1,059.73 (1,071.00) [1,071.00]	549.63 (11.27) [44]
755	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690)	3/2017	3/2020 (-) [5/2020]	1,030.44 (-) [1,065.51]	1,027.16 (35.07) [2]
756	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500)	3/2017	3/2020 (-) [8/2020]	988.34 (-) [1,043.28]	1,094.73 (54.94) [5]
757	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3	8/2015	5/2018 (4/2019) [9/2020]	505.00 (-) [504.00]	220.70 (-1.00) [28]
758	AHMADPUR TO PIMPLA	1/2017	8/2019 (-) [8/2019]	422.38 (422.38) [422.38]	169.58 (0.00) [0]
759	AHMEDNAGAR TO BARAMATI	1/2017	8/2019 (-) [8/2019]	955.40 (-) [955.40]	338.50 (0.00) [0]
760	AKKALKOT TO DHUDHNI	4/2016	2/2019 (-) [2/2020]	211.42 (-) [211.42]	131.85 (0.00) [12]
761	AKOLA TO AKOT	1/2017	6/2019 (-) [0/0]	313.95 (-) [313.95]	37.05 (0.00) [0]
762	AKOT TO ANJANGAON	1/2017	6/2019 (-) [0/0]	245.77 (246.00) [245.77]	182.98 (0.00) [0]
763	AMDNI TO SAONER	1/2017	6/2019 (-) [8/2019]	396.91 (396.91) [396.91]	248.48 (0.00) [0]
764	ARDHAPUR TO HIMAYATNAGAR	12/2017	6/2020 (-) [6/2020]	426.06 (426.00) [426.06]	66.97 (0.00) [0]
765	ARNI TO NAIGAINBANDI	12/2017	12/2019 (-) [12/2019]	309.94 (310.00) [309.94]	51.32 (0.00) [0]
766	AURANGABAD TO SILLOD	2/2017	6/2019 (-) [0/0]	456.32 (-) [456.32]	91.75 (0.00) [0]
767	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62	3/2016	7/2018 (-) [0/0]	197.69 (-) [197.69]	22.27 (0.00) [0]
768	BAMNI TO NAVAEGAON	9/2017	4/2020 (-) [4/2020]	241.69 (242.00) [241.69]	146.29 (0.00) [0]
769	BARASGAON TO RAHATEE	7/2016	9/2018 (-) [4/2021]	289.11 (290.00) [289.11]	148.00 (0.00) [31]
770	BHADGAON TO CHALISGAON	1/2018	11/2019 (-) [11/2019]	259.55 (260.00) [259.55]	145.00 (0.00) [0]
771	BHANDARA TO GHOTITOK	1/2017	6/2019 (-) [0/0]	392.83 (393.00) [392.83]	281.60 (0.00) [0]
772	BHOGAN KHURD TO KASHEDI	9/2017	6/2021	743.21	131.87

			(-) [6/2021]	(743.21) [743.21]	(0.00) [0]
773	BHOKAR TO SARSAM	2/2017	7/2019 (-) [0/0]	295.09 (-) [295.99]	162.64 (0.90) [0]
774	BODHWAD TO STATE BORDER	1/2017	7/2019 (-) [0/0]	178.26 (-) [178.26]	118.95 (0.00) [0]
775	CHALISGAON TO NANDGAON	3/2018	12/2019 (-) [12/2019]	206.97 (207.00) [206.97]	78.89 (0.00) [0]
776	CHIKALI TO DHAD	3/2018	12/2019 (-) [12/2019]	189.46 (189.00) [189.46]	21.54 (0.00) [0]
777	CHIKALI TO KHAMGAON	2/2017	6/2019 (-) [10/2019]	548.03 (548.00) [548.03]	287.00 (0.00) [4]
778	CHIKLI TO TAKARKHED	3/2018	12/2019 (-) [12/2019]	393.10 (393.10) [393.10]	125.97 (0.00) [0]
779	CHIMUR TO WARORA	11/2016	3/2019 (-) [0/0]	467.70 (-) [467.70]	146.72 (0.00) [0]
780	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF	3/2018	/ (-) [7/2021]	1,162.92 (-) [1,162.92]	14.29 (0.00) [-]
781	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	12/2015	3/2019 (4/2021) [4/2021]	649.50 (-) [649.50]	134.58 (0.00) [25]
782	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6)	3/2018	/ (11/2020) [11/2020]	291.53 (-) [291.53]	30.82 (0.00) [-]
783	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST	1/2017	5/2019 (-) [12/2019]	244.90 (-) [244.90]	243.33 (0.00) [7]
784	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH- 53 (OLD NH-6)	3/2018	/ (-) [11/2020]	289.21 (-) [289.21]	27.22 (0.00) [-]
785	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	10/2015	5/2018 (6/2020) [6/2020]	593.26 (41.54) [636.24]	438.73 (42.98) [25]
786	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION	12/2011	/ (-) [0/0]	156.26 (227.00) [247.95]	175.00 (91.69) [0]
787	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	10/2015	5/2018 (-) [9/2020]	531.13 (-) [727.00]	421.65 (195.87) [28]
788	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16)	3/2015	/ (-) [0/0]	168.30 (-) [168.30]	52.00 (0.00) [0]
789	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOIA ROAD FROM KM 161 TO	8/2014	7/2016 (-) [0/0]	187.79 (-) [187.79]	76.62 (0.00) [0]
790	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST	3/2017	3/2020 (2/2021) [2/2020]	247.02 (-) [157.49]	21.89 (-89.53) [-1]
791	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D	9/2015	5/2018 (3/2019) [5/2020]	414.51 (-) [414.00]	531.36 (-0.51) [24]
792	DAHEGAON TO KUHI	1/2017	6/2019 (-)	228.89 (228.89)	125.00 (0.00)

			[0/0]	[228.89]	[0]
793	DASTAPUR TO KARANJA	3/2018	12/2019 (-) [12/2019]	182.63 (-) [182.63]	83.40 (0.00) [0]
794	DEORI TO AMGAON	1/2017	5/2019 (-) [5/2020]	409.62 (410.00) [409.62]	171.78 (0.00) [12]
795	DEULGAON SAKARSHA TO MEHKAR	3/2018	12/2019 (-) [12/2019]	219.91 (-) [219.91]	106.46 (0.00) [0]
796	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000)	3/2017	3/2020 (-) [9/2019]	296.19 (-) [254.00]	248.60 (-42.19) [-6]
797	DHAD BHOKARDAN TO BHOKARDHAN SILLOD	3/2018	12/2019 (-) [12/2019]	336.21 (336.00) [336.21]	64.66 (0.00) [0]
798	DHANGIPIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK	3/2018	2/2020 (-) [2/2020]	217.14 (217.00) [217.14]	66.77 (0.00) [0]
799	DIGRAS DARWAH KARANJA	1/2017	6/2019 (-) [6/2020]	391.06 (391.00) [391.06]	68.00 (0.00) [12]
800	FARDAPUR TO JALGAON	2/2017	6/2019 (-) [0/0]	456.45 (-) [456.45]	56.74 (0.00) [0]
801	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTTEE KANOON AND NAGPUR BYPASS	4/2010	6/2012 (-) [0/0]	1,170.52 (-) [1,170.52]	2,051.36 (0.00) [0]
802	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4	3/2018	/ (-) [12/2020]	642.13 (-) [807.00]	302.29 (164.87) [-]
803	FOUR LANING OF AURANGABAD - YEDISHI	7/2015	1/2018 (12/2018) [12/2019]	1,871.34 (67.34) [1,871.34]	3,495.79 (0.00) [23]
804	FOUR LANNING OF TULJAPUR-AUSA SECTION	2/2017	2/2020 (11/2017) [5/2020]	904.16 (911.07) [904.16]	817.58 (0.00) [3]
805	GADCHIROLI TO MUL	12/2016	6/2019 (-) [0/0]	484.15 (-) [484.15]	160.31 (0.00) [0]
806	HELWAK TO KARAD	2/2017	7/2019 (-) [0/0]	416.99 (-) [416.99]	113.40 (0.00) [0]
807	HIMAYATNAGAR TO PHULSAWANGI	3/2018	12/2019 (-) [12/2019]	294.87 (295.00) [294.87]	12.30 (0.00) [0]
808	INDAPUR TO AGARDANDA	1/2017	7/2019 (-) [12/2019]	355.17 (355.17) [355.17]	164.87 (0.00) [5]
809	INDAPUR TO VADPALE	1/2017	12/2019 (-) [3/2020]	1,202.52 (1,202.52) [1,202.52]	635.90 (0.00) [3]
810	JAHIRABAD TO LATUR	1/2017	11/2019 (-) [11/2019]	461.96 (461.96) [461.96]	151.43 (0.00) [0]
811	JALGAON TO BHADGAON	1/2018	11/2019 (-) [11/2019]	307.54 (308.00) [307.54]	124.59 (0.00) [0]
812	JALGAON TO NANDURA	3/2018	12/2019 (-) [12/2019]	177.84 (177.00) [177.84]	125.69 (0.00) [0]

813	JALKOT TO TOGRI	7/2018	8/2020 (-) [8/2020]	299.92 (300.00) [299.92]	4.20 (0.00) [0]
814	JINTUR TO PARBHANI	1/2017	/	356.66 (356.66) [356.66]	35.88 (0.00) [0]
815	KAJJ TO KUSALAM	1/2017	7/2019 (-) [7/2019]	554.78 (554.78) [554.78]	159.90 (0.00) [0]
816	KALMAB TO RALEGAON	1/2017	6/2019 (-) [0/0]	467.78 (-) [467.78]	294.91 (0.00) [0]
817	KALMATH TO ZARAP	9/2016	3/2020 (-) [3/2020]	1,338.13 (1,338.13) [1,338.13]	959.51 (0.00) [0]
818	KANTE TO WAKED	3/2016	11/2019 (-) [11/2019]	1,230.02 (1,230.02) [1,230.02]	500.61 (0.00) [0]
819	KARAD PATAN CHIPLUN GUHAGAR	2/2017	6/2019 (-) [6/2020]	407.19 (407.00) [407.19]	25.00 (0.00) [12]
820	KARAD TO TAGAON	1/2017	6/2019 (-) [6/2020]	537.81 (538.00) [537.81]	85.97 (0.00) [12]
821	KARAD TO VITA	1/2018	12/2019 (-) [12/2019]	344.85 (245.00) [344.85]	68.04 (0.00) [0]
822	KARWANDI TO RAJURI	3/2018	12/2019 (-) [12/2019]	276.95 (277.00) [276.95]	81.47 (0.00) [0]
823	KATOL TO WARUD	1/2017	6/2019 (-) [8/2019]	463.62 (664.00) [463.62]	257.34 (0.00) [0]
824	KHAMGAON TO DEULGAON SAKARSHA	3/2018	12/2019 (-) [12/2019]	249.29 (-) [249.29]	72.20 (0.00) [0]
825	KHAMGAON TO SHEGAON	2/2017	5/2019 (-) [12/2019]	203.21 (203.00) [203.21]	102.79 (0.00) [7]
826	KHERDA TO NAGZARI	3/2018	12/2019 (-) [12/2019]	181.30 (-) [181.30]	70.50 (0.00) [0]
827	KOLDE TO KHETIYA	1/2017	7/2019 (-) [0/0]	509.18 (-) [509.18]	175.93 (0.00) [0]
828	KOLHA TO NASRATPUR	4/2016	4/2019 (-) [4/2020]	281.78 (282.00) [281.78]	47.73 (0.00) [12]
829	KOTHARI TO DHANORA	9/2018	8/2020 (-) [8/2020]	301.38 (301.00) [301.38]	41.00 (0.00) [0]
830	KUMBHARI PHTA TO DEULGAON RAJA	2/2017	6/2019 (-) [0/0]	406.51 (-) [406.51]	281.03 (0.00) [0]
831	KUNDRAL TO WAZAR	1/2018	12/2019 (-) [12/2019]	225.25 (225.00) [225.25]	121.75 (0.00) [0]
832	KURUDWADI TO PANDHARPUR	1/2017	7/2019 (-) [0/0]	307.63 (-) [307.63]	148.17 (0.00) [0]
833	KUSUMBA TO MALEGAON	3/2018	12/2019	243.45	67.02

			(-) [12/2019]	(244.00) [243.45]	(0.00) [0]
834	LATUR TO PANGAON	3/2018	12/2019 (-) [12/2019]	336.47 (336.00) [336.47]	109.48 (0.00) [0]
835	MAHAD TO RAIGAD FORT	7/2018	5/2020 (-) [5/2020]	237.40 (-) [237.40]	8.34 (0.00) [0]
836	MAJALGAON TO KAIJ	1/2017	7/2019 (-) [7/2019]	413.99 (-) [413.99]	299.33 (0.00) [0]
837	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER	3/2018	12/2019 (-) [12/2019]	256.15 (-) [256.15]	15.50 (0.00) [0]
838	MALEGAON TO RISOD	2/2018	12/2019 (-) [12/2019]	303.24 (303.24) [303.24]	107.97 (0.00) [0]
839	MALEWADA TO CHIMUR	10/2016	6/2019 (-) [6/2020]	322.55 (-) [322.55]	156.91 (0.00) [12]
840	MANGAON TO DIGHI PORT	1/2017	7/2019 (-) [7/2020]	457.52 (457.52) [457.52]	202.98 (0.00) [12]
841	MANGRUPHIR TO MAHAN	3/2018	11/2019 (-) [11/2019]	222.13 (222.13) [222.13]	60.36 (0.00) [0]
842	MANJUSUMBA TO CHUMBALI	1/2017	8/2019 (-) [8/2019]	228.54 (228.54) [228.54]	99.30 (0.00) [0]
843	MANSAR TO SALAIKHURD	1/2018	12/2019 (-) [12/2019]	418.36 (-) [418.36]	116.13 (0.00) [0]
844	MANTHA TALUKAS BORDER TO PARTUR	1/2017	7/2019 (-) [7/2019]	486.19 (486.19) [486.19]	215.29 (0.00) [0]
845	MEHKAR TO AJISPUR	1/2017	7/2019 (-) [0/0]	232.77 (-) [232.77]	85.51 (0.00) [0]
846	MEHKAR TO CHIKALI	2/2017	5/2019 (-) [0/0]	322.48 (322.00) [322.48]	202.08 (0.00) [0]
847	MHASWAD TO TEMBHURNI	1/2017	7/2019 (-) [0/0]	488.60 (-) [488.60]	182.71 (0.00) [0]
848	MORSHI TO ACHALPUR	1/2017	6/2019 (-) [12/2019]	341.16 (341.00) [341.16]	153.29 (0.00) [6]
849	MORSHI TO MAH/MP BORDER	1/2017	6/2019 (-) [0/0]	471.61 (472.00) [471.61]	259.90 (0.00) [0]
850	MUL TO CHANDRAPUR	12/2016	7/2019 (-) [7/2019]	162.34 (-) [162.34]	32.80 (0.00) [0]
851	NAGAJ TO VAIJAPUR	1/2017	6/2019 (-) [12/2019]	376.72 (377.00) [376.72]	168.81 (0.00) [6]
852	NAGBHID TO ARMORI	9/2016	7/2019 (-) [0/0]	269.05 (-) [269.05]	197.91 (0.00) [0]
853	NAGPUR - KONDHALI	9/2005	6/2006 (-)	168.00 (-)	226.24 (0.00)

			[0/0]	[168.00]	[0]
854	NAGPUR RING ROAD PACKAGE-1	3/2016	7/2019 (12/2020) [12/2020]	546.00 (-) [546.00]	269.67 (0.00) [17]
855	NAGPUR RING ROAD PACKAGE-2	3/2016	7/2019 (12/2020) [12/2020]	591.66 (-) [591.66]	310.56 (0.00) [17]
856	NAIGAONBANDI TO MANGRULPIR	12/2017	3/2019 (-) [12/2019]	244.04 (244.00) [244.04]	25.94 (0.00) [9]
857	NALDURG TO AKKALKOT	2/2018	12/2019 (-) [12/2019]	274.50 (275.00) [274.50]	61.39 (0.00) [0]
858	NANDED TO JALKOT	12/2017	9/2019 (-) [9/2019]	456.93 (457.00) [456.93]	54.50 (0.00) [0]
859	NANDGAON TO MORSHI	1/2017	6/2019 (-) [12/2019]	385.87 (386.00) [385.87]	203.75 (0.00) [6]
860	NASHIK TO PETH	12/2015	11/2018 (-) [11/2019]	289.60 (-) [289.60]	118.81 (0.00) [12]
861	NASRATPUR TO BARASGAON	7/2016	9/2019 (-) [9/2019]	406.54 (406.54) [406.54]	142.00 (0.00) [0]
862	NILAJPHATA TO BHANDARA	1/2018	5/2020 (-) [5/2020]	420.63 (421.00) [420.63]	17.60 (0.00) [0]
863	OMREGA TO AUSA	3/2018	12/2019 (-) [12/2019]	272.04 (272.00) [272.04]	124.24 (0.00) [0]
864	OSMANNAGAR TO KUNDRAL	9/2017	8/2020 (-) [8/2020]	344.25 (344.00) [344.25]	33.02 (0.00) [0]
865	PAHUR TO BODHWAD	1/2017	5/2020 (-) [5/2020]	244.93 (-) [244.93]	40.23 (0.00) [0]
866	PAITHAN TO SHIRUR	3/2017	6/2019 (-) [0/0]	341.80 (-) [341.80]	117.89 (0.00) [0]
867	PALPHATA TO PHULAMBARI	3/2018	12/2019 (-) [12/2019]	227.19 (227.00) [227.19]	60.23 (0.00) [0]
868	PANCHARAL TO MANDANGHAR	7/2018	5/2020 (-) [5/2020]	381.08 (302.00) [381.08]	13.00 (0.00) [0]
869	PANDHARPUR TO SANGOLA	7/2017	7/2019 (-) [0/0]	218.38 (-) [218.38]	168.75 (0.00) [0]
870	PARBHANI TO GANGKHED	3/2018	12/2019 (-) [12/2019]	238.19 (238.00) [238.19]	40.85 (0.00) [0]
871	PARLI PIMPLA DAHIGUDA	2/2017	6/2019 (-) [6/2020]	205.72 (205.72) [205.72]	30.42 (0.00) [12]
872	PARSHURAM GHAT TO ARAWALI	4/2016	12/2019 (-) [11/2019]	983.14 (983.14) [983.14]	655.15 (0.00) [-1]
873	PARTUR TO MAJALGAON	1/2017	7/2019 (-) [7/2019]	420.57 (420.57) [420.57]	215.39 (0.00) [0]

874	PATGAON KHOPOLI SECTION I	1/2018	12/2019 (-) [12/2019]	170.00 (-) [170.00]	39.57 (0.00) [0]
875	PEN TO KHOPOLI	3/2018	3/2018 (-) [12/2019]	301.39 (302.00) [301.39]	0.00 (0.00) [21]
876	PIMPLA TO MANJARUMBHA	1/2017	8/2019 (-) [8/2019]	595.77 (595.77) [595.77]	132.44 (0.00) [0]
877	PUNE RAIGARH DISTRICT BORDER TO MANGAON	3/2018	12/2019 (-) [12/2019]	223.46 (-) [223.46]	21.42 (0.00) [0]
878	PUNE TO MALE VILLAGE	3/2018	12/2019 (-) [12/2019]	228.31 (-) [228.31]	13.50 (0.00) [0]
879	PUNE-SATARA(NH-4)	10/2010	3/2013 (-) [12/2019]	1,724.55 (-) [1,724.55]	2,387.46 (0.00) [81]
880	RALEGAON TO RAMTIRTH	1/2017	7/2019 (-) [0/0]	210.81 (-) [210.81]	106.69 (0.00) [0]
881	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00	1/2014	/ (-) [0/0]	446.77 (-) [446.77]	259.50 (0.00) [0]
882	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM	1/2015	/ (-) [0/0]	225.81 (-) [225.81]	85.11 (0.00) [0]
883	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA	3/2016	12/2019 (-) [12/2019]	536.65 (356.00) [536.65]	42.25 (0.00) [0]
884	RISOD TO HINGOLI	2/2018	12/2019 (-) [12/2019]	355.99 (355.99) [355.99]	112.97 (0.00) [0]
885	SAKOLI TO BHANDARA	1/2017	6/2019 (-) [11/2019]	362.96 (362.96) [362.96]	37.83 (0.00) [5]
886	SALAIKHURD TO TIRORA	1/2018	12/2019 (-) [12/2019]	415.25 (415.25) [415.25]	82.22 (0.00) [0]
887	SANGOLA TO JATH	1/2018	12/2019 (-) [12/2019]	257.38 (257.00) [257.38]	61.15 (0.00) [0]
888	SARAD VANI PIMPALGAON	1/2017	7/2019 (-) [0/0]	250.46 (-) [250.46]	103.63 (0.00) [0]
889	SARSAM TO KOTHARI	2/2016	7/2019 (-) [0/0]	545.64 (-) [545.64]	65.01 (0.00) [0]
890	SATARA MURVAD PILLOV PANDHARPUR	1/2017	/ (-) [0/0]	388.44 (-) [388.44]	188.77 (0.00) [0]
891	SATARA TO MHASWAD	1/2017	7/2019 (-) [0/0]	653.46 (-) [653.46]	202.42 (0.00) [0]
892	SELDOH TO PANVAR	7/2018	5/2020 (-) [5/2020]	404.33 (404.00) [404.33]	30.19 (0.00) [0]
893	SHAHPUR PATGAON SECTION I	1/2018	12/2019 (-) [12/2019]	150.79 (150.79) [150.79]	21.42 (0.00) [0]
894	SHEGAON TO DEORI PHATA	2/2017	5/2019	373.10	123.43

			(-) [12/2019]	(373.00) [373.10]	(0.00) [7]
895	SHIROD SHAHPURER TO NANDED	1/2017	7/2019 (-) [7/2019]	211.34 (211.34) [211.34]	101.83 (0.00) [0]
896	SHIRUR TO KHARDA	2/2017	6/2019 (-) [0/0]	381.77 (-) [381.77]	100.79 (0.00) [0]
897	SHIVUR TO YEOLA	3/2018	12/2019 (-) [12/2019]	181.08 (-) [181.08]	2.50 (0.00) [0]
898	SILLOD TO FARDAPUR	2/2017	6/2019 (-) [0/0]	337.46 (-) [337.46]	39.22 (0.00) [0]
899	SIX LANNING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH	12/2017	/ (-) [10/2020]	404.94 (448.18) [448.18]	102.43 (43.24) [-]
900	SIX LANNING FROM EXISTING KM 494.410(DSIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DSIGN CHAINAGE	11/2016	/ (3/2020) [3/2019]	290.73 (315.00) [315.00]	215.98 (24.27) [0]
901	TAKARKHED TO JALNA	9/2017	6/2019 (-) [12/2019]	417.90 (418.00) [417.90]	87.26 (0.00) [6]
902	TALEGAON TO GONAPUR	1/2018	3/2019 (-) [12/2019]	264.41 (264.00) [264.41]	32.71 (0.00) [9]
903	TALGAON TO KALMATH	10/2016	3/2020 (-) [3/2020]	904.70 (904.70) [904.70]	604.05 (0.00) [0]
904	TASGAON TO SHIRDHON	1/2017	11/2019 (-) [11/2019]	195.64 (196.00) [195.64]	169.73 (0.00) [0]
905	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI	2/2017	7/2019 (-) [0/0]	422.02 (422.00) [422.02]	238.01 (0.00) [0]
906	VADPALE TO BHOGAN KHURD	1/2017	11/2019 (-) [3/2020]	1,598.47 (1,598.47) [1,598.47]	751.91 (0.00) [4]
907	VITA TO NAGAJ	3/2018	12/2019 (-) [12/2019]	304.58 (305.00) [304.58]	9.16 (0.00) [0]
908	WADI TO ASOLA	1/2017	9/2019 (-) [9/2020]	363.82 (363.82) [363.82]	41.10 (0.00) [12]
909	WADIGODRI TO DHANGRIPIMPRI	3/2018	2/2020 (-) [2/2020]	194.23 (194.00) [194.23]	68.23 (0.00) [0]
910	WAKAN PALI KHOPOLI	1/2017	5/2019 (-) [5/2020]	376.19 (376.19) [376.19]	29.03 (0.00) [12]
911	WAKED TO TALEGAON	2/2016	2/2019 (-) [0/0]	1,244.75 (1,245.00) [1,244.75]	357.60 (0.00) [0]
912	WARDHA TO ARVI	2/2018	4/2020 (-) [4/2020]	313.58 (313.58) [313.58]	4.96 (0.00) [0]
913	WARDHA TO HINGAGHAT	1/2018	12/2019 (-) [12/2019]	216.90 (216.90) [216.90]	45.00 (0.00) [0]
914	WASHIM TO DASTAPUR	3/2018	12/2019 (-)	165.51 (-)	35.45 (0.00)

			[12/2019]	[165.51]	[0]
915	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16	10/2015	/ (-) [0/0]	289.60 (-) [289.60]	90.65 (0.00) [0]
916	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	5/2013	2/2014 (-) [0/0]	1,348.20 (-) [1,348.20]	1,792.90 (0.00) [0]
	<u>Telecommunications</u>				
917	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	1/2018	10/2018 (12/2019) [12/2019]	231.80 (240.10) [240.10]	117.63 (8.30) [14]
	<u>Urban Development</u>				
918	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI	1/2018	7/2020 (9/2020) [9/2020]	223.37 (-) [223.37]	33.01 (0.00) [2]
919	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	7/2013	1/2015 (-) [5/2020]	23,136.00 (-) [23,136.00]	0.00 (0.00) [64]
920	NAGPUR METRO RAIL	8/2014	3/2018 (-) [12/2019]	8,680.00 (-) [8,680.00]	6,237.34 (0.00) [21]
921	PUNE METRO RAIL PROJECT (PHASE 1)	12/2016	11/2021 (1/2022) [1/2022]	11,420.00 (-) [11,420.00]	2,896.26 (0.00) [2]
922	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA	6/2010	3/2012 (-) [0/0]	205.00 (-) [205.00]	165.47 (0.00) [0]
	<u>Water Resources</u>				
923	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA	3/2017	12/2019 (-) [12/2019]	233.57 (-) [233.57]	32.20 (0.00) [0]
	<u>MANIPUR</u>				
	<u>Power</u>				
924	LOKTAK D/S HEP(NHPC)	12/1999	6/2006 (-) [0/0]	578.62 (-) [578.62]	0.00 (0.00) [0]
	<u>Railways</u>				
925	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (-) [3/2020]	4,454.17 (13,809.00) [12,524.00]	9,123.93 (8,069.83) [108]
	<u>Road Transport And Highways</u>				
926	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260.	10/2016	11/2020 (-) [11/2020]	235.31 (-) [235.31]	91.38 (0.00) [0]
927	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	8/2017	10/2018 (-) [10/2021]	517.57 (-) [457.77]	137.04 (-59.80) [36]
	<u>Urban Development</u>				
928	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	2/2014	3/2015 (-) [10/2020]	216.69 (-) [216.69]	52.00 (0.00) [67]
	<u>MEGHALAYA</u>				
	<u>Health And Family Welfare</u>				
929	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (-) [9/2019]	363.99 (-) [363.99]	166.19 (0.00) [16]
	<u>Railways</u>				
930	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [3/2021]	906.46 (-) [6,000.00]	261.76 (5,093.54) [0]
	<u>Road Transport And Highways</u>				

931	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	3/2019	5/2019 (-) [0/0]	306.28 (-) [306.28]	42.66 (0.00) [0]
932	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	12/2015	5/2018 (3/2018) [10/2019]	479.20 (-) [479.20]	711.38 (0.00) [17]
933	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	/ (-) [9/2021]	553.51 (-) [553.51]	27.90 (0.00) [-]
	<u>Urban Development</u>				
934	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR	4/2014	9/2017 (-) [0/0]	151.33 (-) [151.33]	7.15 (0.00) [0]
	<u>MIZORAM</u>				
	<u>Railways</u>				
935	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (3/2022) [3/2022]	2,393.47 (4,968.00) [5,021.45]	3,075.08 (2,627.98) [96]
	<u>Road Transport And Highways</u>				
936	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (-) [6/2020]	195.04 (-) [377.99]	305.38 (182.95) [116]
937	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	9/2014 (-) [12/2019]	186.96 (-) [305.61]	275.06 (118.65) [63]
938	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (-) [12/2019]	193.69 (-) [327.92]	254.24 (134.23) [110]
939	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	519.09 (-) [519.09]	0.00 (0.00) [0]
940	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	640.07 (-) [640.07]	0.00 (0.00) [0]
941	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	642.96 (-) [642.96]	0.00 (0.00) [0]
942	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	537.82 (-) [537.82]	0.00 (0.00) [0]
943	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	404.29 (-) [404.29]	0.00 (0.00) [0]
944	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	428.11 (-) [428.11]	0.00 (0.00) [0]
945	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	518.53 (-) [518.53]	0.00 (0.00) [0]
946	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	473.18 (-) [473.18]	0.00 (0.00) [0]
947	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (-) [12/2019]	624.41 (-) [992.67]	853.82 (368.26) [105]
	<u>MULTI STATE</u>				
	<u>Coal</u>				
948	DHANKASA UG (1.00 MTY)	9/2016	3/2022 (-) [3/2022]	458.07 (-) [458.07]	20.86 (0.00) [0]
949	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY)	2/2017	3/2021	328.00	160.15

			(-) [3/2021]	(-) [328.00]	(0.00) [0]
950	NILJAI EXPANSION (DEEP) OC (3.5 MTY)	8/2016	3/2022 (-) [3/2022]	319.76 (-) [319.76]	235.33 (0.00) [0]
	<u>Petroleum</u>				
951	50MW WIND ENERGY POWER PROJECT	11/2015	6/2017 (-) [0/0]	500.00 (-) [500.00]	0.00 (0.00) [0]
952	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	1/2015	12/2020 (-) [12/2020]	1,823.00 (3,027.90) [3,027.90]	861.98 (1,204.90) [0]
953	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II	9/2016	12/2019 (-) [12/2019]	571.66 (-) [571.66]	200.97 (0.00) [0]
954	BARAUNI-GUWAHATI PIPELINE	6/2018	12/2021 (-) [12/2021]	3,308.00 (-) [3,308.00]	1,250.10 (0.00) [0]
955	BOKARO-ANGUL PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	3,437.00 (-) [3,437.00]	1,271.51 (0.00) [0]
956	DOBHI-DURGAPUR PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	2,433.00 (-) [2,433.00]	1,441.96 (0.00) [0]
957	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	9/2017	3/2021 (-) [3/2021]	2,677.00 (-) [2,677.00]	894.02 (0.00) [0]
958	JAIPUR-PANIPAT NAPTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE	2/2015	10/2019 (-) [10/2019]	890.00 (-) [887.00]	603.29 (-3.00) [0]
959	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	6/2009	12/2012 (-) [2/2022]	2,915.00 (2,915.00) [3,049.47]	2,524.91 (134.47) [110]
960	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT	7/2015	12/2020 (-) [12/2020]	2,881.40 (-) [2,000.00]	1,285.47 (-881.40) [0]
961	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION	9/2016	6/2020 (-) [6/2020]	1,879.00 (-) [1,879.00]	1,476.87 (0.00) [0]
962	PARADIP HYDERABAD PIPELINE	1/2015	12/2020 (-) [8/2020]	2,321.00 (3,338.00) [3,338.00]	1,820.56 (1,017.00) [-4]
963	PARADIP LPG IMPORT FACILITY	1/2015	7/2018 (-) [10/2020]	690.00 (-) [690.00]	299.12 (0.00) [27]
964	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I)	5/2016	10/2020 (-) [10/2020]	406.00 (-) [406.00]	88.85 (0.00) [0]
965	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	7/2011	3/2017 (-) [12/2019]	352.56 (-) [438.84]	230.43 (86.28) [33]
	<u>Power</u>				
966	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION)	9/2017	9/2019 (-) [2/2020]	198.49 (-) [198.49]	83.31 (0.00) [5]
967	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	12/2018 (-) [12/2020]	4,754.42 (-) [9,072.36]	1,301.58 (4,317.94) [24]
968	EASTERN REGION STRENGTHENING SCHEME XX	11/2017	5/2020 (-) [5/2020]	358.83 (-) [358.83]	121.83 (0.00) [0]

969	EASTERN REGION STRENGTHENING SCHEME -IX	2/2014	2/2016 (-) [6/2019]	196.58 (-) [225.28]	164.27 (28.70) [0]
970	EASTERN REGION STRENGTHENING SCHEME-V	10/2013	4/2016 (-) [11/2019]	1,364.52 (-) [1,891.41]	1,263.11 (526.89) [43]
971	EASTERN REGION STRENGTHENING SCHEME-XII	5/2014	11/2016 (-) [3/2020]	522.29 (-) [546.36]	466.42 (24.07) [40]
972	EASTERN REGION STRENGTHENING SCHEME-XVIII	3/2017	7/2020 (-) [7/2020]	3,500.00 (3,500.00) [3,500.00]	1,758.00 (0.00) [0]
973	EASTERN REGION STRENGTHENING SCHEME XVII(PART B)	2/2017	6/2019 (-) [3/2020]	235.53 (-) [235.53]	124.27 (0.00) [9]
974	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/	2/2017	2/2019 (-) [12/2019]	322.30 (-) [322.30]	158.10 (0.00) [10]
975	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	3/2015	3/2018 (-) [12/2019]	197.40 (-) [197.40]	83.07 (0.00) [21]
976	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D	5/2016	5/2019 (-) [12/2019]	3,519.59 (-) [3,519.59]	2,502.91 (0.00) [7]
977	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR	2/2017	4/2020 (-) [4/2020]	5,070.13 (-) [5,070.13]	2,771.21 (0.00) [0]
978	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR- SCHEME-I: RAIGARH-P	5/2016	11/2019 (-) [11/2019]	14,733.37 (-) [14,733.37]	8,796.37 (0.00) [0]
979	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN	8/2017	2/2020 (-) [2/2020]	1,931.39 (-) [1,931.39]	1,054.28 (0.00) [0]
980	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION	3/2017	6/2019 (-) [6/2019]	251.60 (-) [251.60]	191.96 (0.00) [0]
981	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	12/2014	12/2018 (-) [12/2020]	5,111.33 (-) [6,880.36]	1,641.35 (1,769.03) [24]
982	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	2/2009	8/2013 (-) [3/2022]	11,130.19 (-) [14,719.10]	12,814.08 (3,588.91) [103]
983	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO	3/2017	11/2019 (-) [11/2019]	283.72 (-) [283.72]	193.70 (0.00) [0]
984	SOUTHERN REGION STRENGTHENING SCHEME-XXI	9/2016	3/2019 (-) [11/2019]	562.25 (-) [562.25]	414.25 (0.00) [8]
985	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	12/2015	4/2019 (-) [11/2019]	3,654.00 (-) [3,654.00]	3,427.57 (0.00) [7]
986	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	10/2016	4/2019 (-) [11/2019]	608.24 (-) [608.24]	413.61 (0.00) [7]
987	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII	1/2015	7/2017 (-) [10/2019]	203.28 (-) [260.03]	193.57 (56.75) [27]
988	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII	3/2017	12/2019 (-) [12/2019]	379.95 (-) [379.95]	76.66 (0.00) [0]
989	SYSTEM STRENGTHENING SCHEME IN NORTHERN	3/2017	6/2019	337.75	92.75

	REGION XXXVIII		(-) [12/2019]	(-) [337.75]	(0.00) [6]
990	SYTEM STRENGTHENING XIII OF SR GRID	10/2011	6/2014 (-) [10/2019]	487.49 (-) [639.46]	564.32 (151.97) [64]
991	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	10/2008	10/2012 (-) [12/2019]	4,824.12 (-) [5,071.94]	4,565.74 (247.82) [86]
992	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP	1/2015	3/2018 (-) [6/2019]	268.80 (-) [340.88]	257.89 (72.08) [0]
993	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP)	1/2015	10/2017 (-) [11/2019]	871.62 (-) [871.62]	582.02 (0.00) [25]
994	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II)	10/2016	1/2019 (-) [12/2019]	408.46 (-) [408.46]	288.56 (0.00) [11]
995	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH	6/2014	3/2018 (-) [12/2019]	5,151.37 (-) [5,151.37]	3,153.93 (0.00) [21]
996	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	3/2016	1/2018 (-) [3/2020]	808.63 (-) [808.63]	525.58 (0.00) [26]
997	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	1/2014	4/2016 (-) [12/2019]	374.63 (-) [374.63]	213.02 (0.00) [44]
998	WESTERN REGION STRENGTHENING SCHEME XVIII	2/2017	2/2020 (-) [2/2020]	195.05 (-) [195.05]	120.83 (0.00) [0]
	<u>Railways</u>				
999	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT	12/2015	12/2023 (12/2023) [12/2023]	1,08,000.00 (-) [1,08,000.00]	4,886.79 (0.00) [0]
1000	BANDEL-BOINCHI 3RD LINE	4/2011	/ (-) [3/2020]	288.35 (-) [382.90]	382.90 (94.55) [-]
1001	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT	4/2007	/ (-) [3/2025]	450.55 (-) [250.55]	20.12 (-200.00) [-]
1002	BHADRACHALAM ROAD-SATTUPALLI	4/2010	3/2020 (-) [3/2020]	704.31 (-) [1,352.74]	269.07 (648.43) [0]
1003	BHADRACHALAM-KOVVUR	4/2012	/ (-) [0/0]	923.23 (-) [1,787.00]	2.46 (863.77) [0]
1004	BOINCHI-SHAKTIGARH 3RD LINE	4/2011	/ (-) [3/2021]	175.80 (-) [245.41]	245.41 (69.61) [-]
1005	CHANDIGARH-BADDI	4/2007	3/2023 (-) [3/2023]	328.14 (-) [1,540.00]	233.84 (1,211.86) [0]
1006	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA	4/2003	/ (-) [3/2025]	337.96 (-) [336.96]	70.20 (-1.00) [-]
1007	CHENNAI-CUDDALORE VIA MAMALLAPURAM	4/2008	/ (-) [0/0]	523.52 (-) [2,300.00]	2.28 (1,776.48) [0]
1008	CHHAPRA-BALLIA UP	3/2013	1/2019 (-) [1/2020]	295.00 (-) [477.31]	328.19 (182.31) [12]
1009	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ	3/2007	12/2021	243.78	106.55

	UP		(-) [12/2021]	(-) [895.00]	(651.22) [0]
1010	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	4/2005	3/2017 (-) [3/2025]	595.51 (-) [769.40]	102.47 (173.89) [96]
1011	CHOTTAUDEPUR-DHAR(NL)	4/2007	3/2022 (3/2022) [3/2022]	1,347.26 (1,347.26) [1,347.26]	724.63 (0.00) [0]
1012	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	4/2007	3/2022 (3/2023) [3/2023]	1,640.04 (1,640.04) [1,640.04]	682.91 (0.00) [12]
1013	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL	4/2010	3/2017 (-) [3/2025]	365.17 (-) [296.43]	234.43 (-68.74) [96]
1014	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL	4/2007	/ (-) [3/2022]	336.91 (-) [800.00]	512.67 (463.09) [-]
1015	DEOGHAR - SULTANGANJ (INL), ER	4/2000	2/2013 (-) [3/2024]	607.09 (-) [1,425.44]	637.42 (818.35) [133]
1016	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR- BANSI PAHARPUR	4/2010	/ (-) [0/0]	2,030.50 (-) [2,030.50]	19.07 (0.00) [0]
1017	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	4/2010	3/2015 (-) [0/0]	651.00 (-) [1,009.00]	7.96 (358.00) [0]
1018	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	/ (-) [0/0]	11,589.00 (30,357.00) [28,181.00]	0.00 (16,592.00) [0]
1019	GAYA-CHATRA (NL)	4/2008	/ (-) [3/2024]	415.67 (-) [549.75]	15.54 (134.08) [-]
1020	GONDIA-JABALPUR(GC),(SECR)	2/1997	4/2020 (12/2020) [12/2020]	511.86 (1,756.92) [1,756.92]	1,661.79 (1,245.06) [8]
1021	GOOTY-DHARMAVARAM-BANGLORE	4/2015	/ (-) [0/0]	636.38 (-) [636.38]	0.00 (0.00) [0]
1022	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	4/2011	3/2022 (-) [12/2024]	2,912.96 (-) [3,845.60]	137.90 (932.64) [33]
1023	HAJIPUR - BACHAWARA	5/2015	3/2019 (-) [2/2021]	678.54 (678.54) [678.54]	492.44 (0.00) [23]
1024	HANSDIHA-GODDA NL	4/2011	3/2020 (-) [3/2021]	542.18 (-) [693.80]	443.81 (151.62) [12]
1025	HANSNABAD-HINGALGANJ NEW BG LINE	4/2010	/ (-) [3/2025]	172.03 (-) [260.10]	10.73 (88.07) [-]
1026	HATHUA-BHATNI (N L) (NER)	4/2005	12/2022 (-) [12/2022]	230.03 (-) [230.03]	277.14 (0.00) [0]
1027	HOTGI-KUDGI-GADAG	3/2015	3/2019 (-) [3/2021]	1,614.59 (-) [1,870.41]	914.00 (255.82) [24]
1028	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS)	4/2010	11/2018 (-) [3/2021]	157.94 (-) [157.94]	51.75 (0.00) [28]
1029	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGREGATION OF AARIVAL/DEPARTURE AND OTHER	4/2011	/ (-)	166.89 (-)	0.02 (0.00)

	AMENITIES		[3/2025]	[166.89]	[-]
1030	JALANDHAR-PATHANKOT-JAMMU TAWI	3/2002	3/2016 (-) [3/2021]	625.00 (-) [845.58]	834.59 (220.58) [60]
1031	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	4/2008	3/2014 (-) [3/2024]	2,132.77 (-) [2,132.77]	331.17 (0.00) [120]
1032	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3	4/2001	3/2016 (-) [3/2025]	923.52 (-) [995.10]	448.78 (71.58) [108]
1033	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE	4/2010	/ (-) [3/2025]	174.56 (-) [174.56]	71.42 (0.00) [-]
1034	KAZIPET-BALHRSHA	4/2015	3/2021 (-) [3/2023]	2,063.03 (-) [2,063.03]	675.97 (0.00) [24]
1035	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	4/2012	3/2023 (-) [3/2024]	1,856.95 (-) [2,200.00]	252.81 (343.05) [12]
1036	KURUPPANTHARA-CHINGAVANAM	4/2007	/ (-) [0/0]	270.14 (457.08) [457.08]	373.51 (186.94) [0]
1037	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP- BUDAKHALI AND CHANDRANAG	4/1987	3/2006 (-) [3/2025]	406.99 (-) [545.70]	148.43 (138.71) [228]
1038	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	9/1998	5/2008 (-) [3/2023]	247.66 (-) [6,093.31]	1,835.18 (5,845.65) [178]
1039	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI- JONGALPARA-FURFURA SHARIF NL	4/2009	3/2014 (-) [3/2025]	257.42 (-) [257.42]	106.51 (0.00) [132]
1040	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	4/2011	3/2019 (-) [12/2019]	120.70 (-) [1,800.00]	170.47 (1,679.30) [9]
1041	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	4/2009	2/2012 (-) [3/2025]	499.96 (-) [680.68]	158.60 (180.72) [157]
1042	MONIGRAM- NIMTITA	4/2012	/ (-) [3/2024]	250.93 (-) [310.70]	263.08 (59.77) [-]
1043	MUNEERABAD-MAHABOBNAGAR(NL),SCR	4/1997	3/2000 (-) [3/2021]	1,723.00 (1.00) [1,723.00]	1,368.46 (0.00) [252]
1044	MURKONGSELEK-PASIGHAT NL	4/2011	3/2020 (-) [3/2020]	414.84 (-) [661.00]	122.05 (246.16) [0]
1045	NANGALDAM-TALWARA(NL),NR	3/1981	7/2012 (-) [3/2024]	450.00 (-) [2,010.00]	654.07 (1,560.00) [140]
1046	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI- BAHRAHAT NL	4/2010	3/2005 (-) [3/2025]	494.54 (-) [494.59]	32.00 (0.05) [240]
1047	NEW BG LINE FROM BALURGHAT TO HILLY NFR	4/2010	3/2020 (-) [3/2020]	242.22 (-) [471.00]	68.15 (228.78) [0]
1048	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	4/2010	/ (-) [3/2021]	241.52 (-) [394.28]	272.88 (152.76) [-]
1049	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	4/2013	3/2019 (-) [0/0]	1,798.00 (-) [2,496.67]	0.00 (698.67) [0]

1050	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	4/1999	/ (-) [0/0]	819.23 (-) [1,871.00]	1,082.01 (1,051.77) [0]
1051	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	4/2000	12/2008 (-) [3/2021]	1,180.19 (3,300.00) [4,541.00]	3,279.71 (3,360.81) [147]
1052	PHULERA - DIGANA DOUBLING	5/2015	3/2020 (-) [4/2022]	600.00 (-) [685.99]	47.07 (85.99) [25]
1053	PIRPAINTI-BHAGALPUR	4/2011	/ (-) [5/2019]	261.38 (-) [471.81]	467.50 (210.43) [0]
1054	PIRPAINTI-JASIDIH	4/2013	3/2022 (-) [3/2025]	915.98 (-) [2,137.81]	294.91 (1,221.83) [36]
1055	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY	4/2011	3/2017 (-) [3/2026]	299.60 (-) [335.62]	1.12 (36.02) [108]
1056	RATLAM-DUNGARPUR VIA BANSWARA (NL)	4/2011	/ (-) [0/0]	2,082.75 (-) [4,079.15]	185.11 (1,996.40) [0]
1057	RAYADURGA-TUMKUR NL	4/2007	/ (-) [3/2022]	2,062.30 (-) [2,062.20]	825.58 (-0.10) [-]
1058	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL	4/2000	/ (-) [3/2025]	297.47 (-) [298.22]	52.09 (0.75) [-]
1059	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	4/2010	3/2016 (-) [3/2025]	277.28 (-) [266.32]	160.40 (-10.96) [108]
1060	SRINIVASA-PURA-MADANAPALLI NL	4/2013	/ (-) [12/2023]	296.00 (-) [466.65]	0.00 (170.65) [-]
1061	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR	4/2007	/ (-) [3/2025]	450.00 (-) [1,261.34]	0.00 (811.34) [-]
1062	TARAKESHWAR-MAGRA NEW BG LINE	4/2010	/ (-) [3/2025]	365.17 (-) [527.54]	1.76 (162.37) [-]
1063	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	3/2020 (-) [3/2020]	16,592.00 (51,101.00) [51,101.00]	22,485.00 (34,509.00) [0]
1064	YELAHANKA-PENUKONDA	5/2015	3/2020 (-) [3/2020]	860.43 (-) [860.43]	697.21 (0.00) [0]
	Road Transport And Highways				
1065	4 LANING OF NAGPUR-BETUL	2/2011	8/2014 (-) [0/0]	2,498.76 (-) [2,498.76]	2,531.46 (0.00) [0]
1066	DELHI AGRA APPROVED LENGTH 180.0 KM	10/2012	4/2015 (-) [0/0]	1,928.22 (-) [2,945.00]	3,070.11 (1,016.78) [0]
1067	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III)	9/2015	3/2018 (-) [0/0]	788.51 (-) [788.51]	103.37 (0.00) [0]
1068	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67.	3/2018	/ (-) [0/0]	1,294.47 (-) [1,296.00]	0.00 (1.53) [0]
1069	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE	3/2018	/ (-) [0/0]	998.70 (-) [962.00]	0.00 (-36.70) [0]

1070	GWALIOR-JHANSI, NH-75	12/2003	12/2009 (-) [8/2020]	604.00 (-) [604.00]	423.83 (0.00) [128]
1071	MUZAFFARNAGAR-HARIDWAR	9/2011	3/2013 (-) [12/2019]	754.00 (-) [754.00]	1,364.18 (0.00) [81]
1072	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP	9/2016	/ (-) [2/2020]	1,244.10 (-) [1,244.10]	1,335.00 (0.00) [-]
1073	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	2/2009	8/2011 (-) [0/0]	1,693.75 (2,848.49) [1,693.75]	2,848.49 (0.00) [0]
1074	VARANASI-AURANGABAD KM.786 TO KM.978.40	9/2011	3/2014 (-) [12/2019]	2,848.00 (-) [2,848.00]	1,159.10 (0.00) [69]
	Shipping And Ports				
1075	JAL MARG VIKAS PROJECT	1/2018	3/2023 (3/2023) [3/2023]	4,200.00 (5,369.18) [5,369.18]	1,400.95 (1,169.18) [0]
	Telecommunications				
1076	NETWORK FOR SPECTRUM	3/2012	7/2015 (-) [5/2020]	13,334.00 (-) [24,664.00]	8,397.00 (11,330.00) [58]
1077	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY	9/2014	9/2014 (-) [0/0]	2,111.17 (-) [2,011.17]	253.90 (-100.00) [0]
	NAGALAND				
	Railways				
1078	DIMAPUR-TIZIT NL	4/2013	3/2020 (-) [3/2020]	4,274.00 (-) [4,274.00]	0.00 (0.00) [0]
1079	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015 (-) [10/2021]	2,326.52 (-) [4,600.00]	781.71 (2,273.48) [79]
	Road Transport And Highways				
1080	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018 (5/2019) [0/0]	239.30 (-) [239.30]	0.00 (0.00) [0]
1081	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	3/2018	9/2018 (-) [0/0]	285.68 (-) [285.68]	0.00 (0.00) [0]
1082	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	3/2018	9/2018 (11/2018) [0/0]	282.98 (-) [282.98]	12.76 (0.00) [0]
1083	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018 (-) [0/0]	387.00 (-) [387.00]	135.12 (0.00) [0]
1084	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	9/2018 (-) [0/0]	500.09 (-) [500.09]	0.00 (0.00) [0]
1085	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN	3/2017	11/2020 (-) [11/2020]	217.35 (-) [217.35]	35.10 (0.00) [0]
1086	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683	2/2017	4/2017 (-) [0/0]	507.68 (-) [507.68]	129.13 (0.00) [0]
1087	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (7/2019) [0/0]	339.57 (233.35) [339.57]	0.00 (0.00) [0]
1088	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM	3/2018	9/2018 (-)	315.03 (-)	4.38 (0.00)

	79.040 TO		[0/0]	[315.03]	[0]
1089	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	9/2018 (-) [0/0]	240.64 (-) [240.64]	2.11 (0.00) [0]
1090	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [0/0]	215.12 (-) [215.12]	10.07 (0.00) [0]
1091	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	9/2018 (-) [0/0]	215.79 (-) [215.79]	0.00 (0.00) [0]
1092	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [0/0]	272.89 (-) [272.89]	0.00 (0.00) [0]
1093	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	3/2018	9/2018 (-) [0/0]	323.98 (-) [323.98]	0.00 (0.00) [0]
1094	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0	3/2018	9/2018 (11/2018) [0/0]	251.97 (160.10) [251.97]	16.63 (0.00) [0]
1095	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (11/2018) [0/0]	237.72 (136.73) [237.72]	21.71 (0.00) [0]
1096	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	8/2016 (-) [8/2019]	373.07 (387.00) [373.07]	209.22 (0.00) [0]
1097	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2016 (-) [6/2020]	396.52 (339.55) [396.52]	234.03 (0.00) [46]
1098	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	3/2016	8/2016 (-) [8/2019]	429.52 (340.00) [429.52]	166.55 (0.00) [0]
1099	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M	11/2016	9/2019 (-) [9/2019]	336.25 (369.96) [336.25]	62.64 (0.00) [0]
1100	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (-) [12/2020]	167.62 (-) [167.62]	42.15 (0.00) [0]
1101	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (-) [12/2020]	172.63 (-) [172.63]	45.02 (0.00) [0]
1102	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA	12/2010	2/2011 (-) [0/0]	1,296.00 (-) [1,296.00]	0.00 (0.00) [0]
1103	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH-	3/2019	12/2022 (-) [12/2022]	237.51 (-) [237.51]	0.00 (0.00) [0]
	<u>ODISHA</u>				
	<u>Coal</u>				
1104	ANANTA OC EXPANSION PH-III (15.0 MTY)	8/2008	3/2012 (-) [3/2021]	207.28 (-) [207.28]	228.90 (0.00) [108]
1105	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	3/2010 (-) [3/2022]	172.08 (-) [172.08]	347.15 (0.00) [144]
1106	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	5/2014	3/2019 (-) [3/2022]	479.15 (-) [479.15]	200.65 (0.00) [36]
1107	BHUBANESWARI OCP, MCL (20.0 MTY)	12/2007	3/2017 (-) [3/2020]	490.10 (-) [490.10]	501.82 (0.00) [36]
1108	GARJANBAHAL OCP	11/2014	3/2021	1,375.38	440.13

			(-) [3/2021]	(-) [1,375.38]	(0.00) [0]
1109	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	3/2013 (-) [3/2021]	479.53 (-) [479.53]	390.94 (0.00) [96]
1110	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP	5/2018	3/2027 (-) [3/2027]	2,434.75 (-) [2,434.75]	83.20 (0.00) [0]
1111	JAGANNATH RE-ORGANISATION OC.(6.00 MTY)	5/2014	3/2019 (-) [3/2020]	337.66 (-) [337.66]	183.98 (0.00) [12]
1112	KANIHA OCP, MCL, (10.0 MTY)	12/2007	3/2013 (-) [3/2022]	457.77 (-) [457.77]	539.59 (0.00) [108]
1113	KULDA EXPN OC. (5.00 MTY)	6/2014	3/2018 (-) [3/2020]	289.03 (-) [289.03]	75.85 (0.00) [24]
1114	KULDA OCP (MAHANADI COALFIELDS LTD)	1/2005	3/2010 (-) [3/2020]	302.96 (-) [302.96]	302.96 (0.00) [120]
1115	REORGANISATION OF BHARATPUR OCP EXPANSION	11/2018	3/2029 (-) [3/2029]	2,838.87 (-) [2,838.87]	1,113.66 (0.00) [0]
1116	SIARMAL OCP (40.00MTY)	5/2014	3/2026 (-) [3/2026]	3,756.36 (-) [3,756.36]	1,549.76 (0.00) [0]
	Mines				
1117	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/2014	4/2021 (4/2021) [4/2021]	5,540.00 (5,540.00) [5,540.00]	107.45 (0.00) [0]
1118	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	12/2015	11/2020 (-) [11/2020]	355.00 (-) [355.00]	31.92 (0.00) [0]
1119	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN	11/2017	4/2021 (4/2021) [4/2021]	483.00 (483.00) [483.00]	0.30 (0.00) [0]
1120	UTKAL D AND E COAL BLOCK	5/2016	1/2020 (-) [1/2020]	534.00 (-) [534.00]	319.23 (0.00) [0]
	Petroleum				
1121	2G ETHANOL BIO REFINERY AT BARGARH	8/2017	12/2020 (-) [12/2020]	750.00 (-) [750.00]	34.73 (0.00) [0]
1122	ADDITIONAL STORAGE TANKS AT PARADIP	11/2018	9/2021 (-) [9/2021]	462.30 (-) [462.30]	0.00 (0.00) [0]
1123	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY	8/2017	12/2021 (-) [12/2020]	315.00 (-) [315.00]	112.13 (0.00) [-12]
1124	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR	7/2017	7/2022 (-) [7/2022]	243.53 (-) [243.53]	52.38 (0.00) [0]
1125	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK	7/2017	7/2022 (-) [7/2022]	182.20 (-) [182.20]	30.42 (0.00) [0]
1126	DHAMRA-ANGUL PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	1,933.00 (-) [1,933.00]	1,035.77 (0.00) [0]
1127	ETHYLENE GLYCOL PROJECT AT PARADIP	4/2018	10/2021 (-) [10/2021]	5,654.00 (-) [5,654.00]	344.69 (0.00) [0]

1128	Fuel Quality Upgradation Project at Paradip Refinery	5/2019	8/2021 (-) [8/2021]	3,361.00 (-) [3,361.00]	325.72 (0.00) [0]
1129	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY	5/2016	1/2019 (-) [12/2019]	429.00 (-) [429.00]	311.78 (0.00) [11]
1130	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY	6/2019	9/2022 (-) [9/2022]	371.00 (-) [371.00]	0.00 (0.00) [0]
1131	LPG BP PROJECT KHORDHA	12/2016	12/2019 (-) [7/2021]	161.59 (-) [161.59]	38.29 (0.00) [19]
1132	PARADIP SOMNATHPUR HALDIA PIPELINE	10/2018	10/2021 (-) [10/2021]	1,297.50 (-) [1,297.50]	10.17 (0.00) [0]
1133	POLYPROPYLENE PLANT AT PARADIP REFINERY	3/2014	9/2017 (-) [7/2019]	3,150.00 (-) [3,150.00]	2,573.02 (0.00) [0]
	<u>Power</u>				
1134	DARLIPALLI STPP STAGE-I (2X800 MW)	2/2014	12/2018 (2/2020) [9/2020]	12,532.44 (-) [13,740.53]	9,726.03 (1,208.09) [21]
1135	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA	4/2016	4/2019 (-) [11/2019]	844.64 (-) [844.64]	435.06 (0.00) [7]
1136	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL	5/2016	12/2018 (-) [3/2020]	1,885.13 (-) [1,885.13]	527.90 (0.00) [15]
	<u>Railways</u>				
1137	BANASPANI- JAKHPURA - DOUBLING	3/2009	3/2019 (-) [6/2022]	942.95 (-) [1,120.00]	1,010.21 (177.05) [39]
1138	BHADRAK - NERGUNDI 3RD LINE	3/2013	10/2020 (3/2023) [3/2023]	843.04 (-) [843.04]	133.25 (0.00) [29]
1139	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	4/2015	12/2018 (3/2022) [3/2022]	1,172.92 (-) [1,172.92]	397.91 (0.00) [39]
1140	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION	4/2010	3/2015 (-) [0/0]	149.90 (-) [230.00]	54.46 (80.10) [0]
1141	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL	4/2016	3/2020 (-) [6/2023]	5,200.00 (-) [1,700.43]	48.00 (-3,499.57) [39]
1142	HARIDASPUR-PARADEEP(NL)	4/1996	12/2017 (-) [3/2020]	1,185.64 (-) [1,844.47]	1,783.59 (658.83) [27]
1143	JAGADALPUR-KORAPUT DOUBLING	4/2015	3/2022 (-) [3/2023]	1,547.38 (-) [1,547.38]	346.97 (0.00) [12]
1144	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	4/2015	11/2018 (-) [3/2022]	701.61 (-) [810.02]	122.59 (108.41) [40]
1145	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	4/2000	3/2009 (3/2009) [12/2019]	133.41 (207.00) [385.00]	386.30 (251.59) [129]
1146	KHURDA ROAD-BOLANGIR(NL)ECOR	4/1994	3/2009 (-) [6/2024]	2,923.13 (-) [3,791.66]	1,237.04 (868.53) [183]
1147	KORAPUT - SINGAPUR ROAD DOUBLING	4/2015	3/2022 (-)	2,361.74 (-)	162.82 (0.00)

			[3/2025]	[2,361.74]	[36]
1148	ROURKELA JHARSUGUDA THIRD LINE 101 KM	11/2015	3/2020 (-) [6/2020]	969.83 (1,312.96) [1,312.96]	549.97 (343.13) [3]
1149	SAMBALPUR - ANGUL RLY. ELECTRIFICATION	3/2012	3/2020 (-) [3/2021]	155.81 (-) [238.03]	226.50 (82.22) [12]
1150	SAMBALPUR - TITLAGARH - DOUBLING	3/2006	3/2020 (-) [3/2021]	948.04 (-) [1,500.00]	1,323.18 (551.96) [12]
1151	SAMBALPUR-TALCHER DOUBLING	3/2011	2/2019 (-) [3/2022]	1,111.99 (-) [1,539.28]	924.93 (427.29) [37]
1152	SUKINDA ROAD - ANGUL (NL)(ECOR)	4/1998	2/2015 (-) [12/2021]	1,202.70 (-) [1,202.70]	914.39 (0.00) [82]
1153	TALCHER-BIMALAGARH(NL)(ECOR)	4/2005	6/2021 (-) [6/2024]	810.78 (-) [1,928.07]	691.04 (1,117.29) [36]
1154	VIZIANAGARAM -SAMABALPUR 3RD LINE	1/1991	12/2024 (-) [12/2024]	2,335.67 (-) [2,335.68]	598.12 (0.01) [0]
	<u>Road Transport And Highways</u>				
1155	4 LANING OF BAHARAGORA - SINGHARA	7/2015	/ (-) [4/2020]	1,282.94 (-) [1,282.94]	210.80 (0.00) [-]
1156	DEVELOPMENT OF FOUR LANNING OF ANGUL- SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S	9/2016	8/2019 (-) [3/2021]	2,510.04 (-) [2,510.04]	252.10 (0.00) [19]
1157	FOUR LANING WITH PS TALEBANI -SMBALPUR	12/2015	/ (-) [11/2019]	752.28 (-) [752.28]	0.00 (0.00) [-]
1158	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION	2/2016	/ (-) [3/2020]	1,069.65 (-) [1,069.65]	502.75 (0.00) [-]
1159	PANIKHOLI-RIMOLI	3/2012	9/2014 (-) [0/0]	1,410.00 (-) [1,410.00]	1,935.14 (0.00) [0]
1160	REHABILITAITON AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4	10/2016	/ (-) [3/2021]	1,008.96 (-) [1,008.96]	469.78 (0.00) [-]
1161	REHABILITATION AND UP GRADATION OF EXISTING 2- LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS	1/2018	/ (-) [8/2021]	564.66 (-) [564.66]	21.00 (0.00) [-]
1162	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	7/2017	7/2017 (11/2020) [6/2021]	476.56 (-) [476.56]	0.00 (0.00) [47]
1163	REHABILITATION AND UP-GRADATION OF EXISTING 2- LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (	1/2018	/ (-) [0/0]	633.68 (-) [633.68]	0.00 (0.00) [0]
1164	REHABILITATION AND UP-GRADATION OF EXISTING 2- LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25	1/2018	/ (5/2020) [6/2021]	953.09 (-) [953.09]	109.21 (0.00) [-]
1165	REHABILITATION AND UP-GRADATION OF EXISTING 2- LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2	1/2018	/ (5/2020) [6/2021]	668.86 (-) [668.86]	109.20 (0.00) [-]
1166	REHABILITATION AND UP-GRADATION OF EXISTING 2- LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG	1/2018	/ (-) [8/2021]	614.48 (-) [614.48]	31.00 (0.00) [-]
1167	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN	7/2014	1/2017 (-)	342.05 (-)	258.91 (0.00)

	TH		[0/0]	[342.05]	[0]
1168	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM	1/2018	/ (-) [0/0]	1,522.00 (-) [1,522.00]	0.00 (0.00) [0]
1169	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (	1/2018	/ (-) [6/2021]	503.88 (-) [503.88]	0.00 (0.00) [-]
1170	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	3/2017	3/2020 (-) [3/2021]	1,288.07 (-) [1,420.00]	365.00 (131.93) [12]
1171	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO	12/2017	/ (7/2020) [6/2021]	686.65 (-) [686.65]	80.87 (0.00) [-]
1172	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON	1/2018	/ (3/2020) [6/2021]	686.65 (-) [686.65]	75.79 (0.00) [-]
1173	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA	12/2017	/ (-) [6/2021]	417.51 (-) [417.51]	8.42 (0.00) [-]
1174	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN	7/2014	1/2017 (-) [0/0]	342.05 (342.00) [342.00]	258.91 (-0.05) [0]
1175	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141	1/2018	/ (-) [0/0]	999.00 (-) [999.00]	0.00 (0.00) [0]
1176	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR	8/2013	6/2016 (-) [11/2019]	171.96 (172.00) [172.00]	88.30 (0.04) [41]
1177	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB	1/1991	10/2017 (-) [0/0]	218.63 (-) [218.63]	29.27 (0.00) [0]
1178	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK	1/1991	5/2018 (-) [0/0]	229.41 (-) [229.41]	6.65 (0.00) [0]
1179	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	12/2011	6/2014 (-) [3/2019]	1,047.00 (-) [1,047.00]	1,874.43 (0.00) [0]
1180	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000)	3/2018	/ (-) [4/2021]	806.11 (-) [806.11]	6.78 (0.00) [-]
1181	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO	3/2014	5/2016 (-) [12/2019]	191.50 (192.00) [192.00]	136.19 (0.50) [43]
1182	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM	2/2015	10/2017 (-) [0/0]	239.91 (240.00) [160.00]	147.25 (-79.91) [0]
1183	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY	1/2015	4/2018 (-) [0/0]	326.63 (327.00) [326.63]	249.26 (0.00) [0]
1184	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG	6/2016	6/2018 (-) [0/0]	157.30 (157.00) [157.30]	97.29 (0.00) [0]
1185	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA	12/2011	11/2017 (-) [9/2019]	159.39 (-) [159.39]	210.29 (0.00) [22]
1186	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA	12/2011	8/2015 (-) [12/2019]	191.08 (-) [191.08]	99.98 (0.00) [52]
1187	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA.	8/2016	2/2017 (-) [0/0]	287.70 (-) [287.70]	153.90 (0.00) [0]

1188	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA	3/2018	8/2018 (-) [0/0]	214.23 (-) [214.23]	23.44 (0.00) [0]
1189	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26.	3/2016	12/2016 (-) [0/0]	165.06 (-) [165.06]	92.59 (0.00) [0]
1190	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA	12/2016	8/2018 (-) [0/0]	223.50 (-) [223.50]	44.52 (0.00) [0]
1191	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA	3/2018	8/2018 (-) [0/0]	199.16 (-) [199.16]	25.63 (0.00) [0]
1192	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA	9/2016	2/2017 (-) [0/0]	295.67 (-) [295.67]	127.75 (0.00) [0]
1193	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA	12/2016	4/2018 (-) [0/0]	206.88 (-) [206.88]	41.69 (0.00) [0]
	<u>Steel</u>				
1194	INSTALLATION OF NEW HOT STRIP MILL AT RSP	4/2015	4/2018 (11/2019) [11/2019]	3,127.30 (-) [3,127.30]	3,031.06 (0.00) [19]
	<u>Urban Development</u>				
1195	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR	1/2019	3/2022 (-) [3/2022]	790.79 (-) [800.00]	2.56 (9.21) [0]
	<u>PUNJAB</u>				
	<u>Fertilisers</u>				
1196	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA	1/2018	11/2019 (-) [11/2019]	218.83 (-) [218.83]	119.23 (0.00) [0]
1197	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL	1/2018	11/2019 (-) [11/2019]	239.81 (-) [239.81]	134.46 (0.00) [0]
	<u>Health And Family Welfare</u>				
1198	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	7/2016	6/2020 (-) [8/2020]	703.00 (-) [703.00]	184.93 (0.00) [2]
1199	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	7/2016	2/2018 (-) [9/2019]	152.95 (-) [152.95]	118.23 (0.00) [19]
	<u>Railways</u>				
1200	QADIAN-BEAS	4/2011	/ (-) [3/2024]	205.22 (-) [205.22]	1.89 (0.00) [-]
	<u>Road Transport And Highways</u>				
1201	4 LANING FROM PHAGWARA TO RUPNAGAR	8/2016	/ (-) [4/2020]	1,169.61 (1,367.00) [1,169.61]	1,063.10 (0.00) [-]
1202	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600	11/2015	/ (9/2019) [0/0]	847.02 (-) [847.02]	1,086.49 (0.00) [0]
1203	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00	11/2015	/ (12/2019) [0/0]	889.24 (-) [904.82]	722.92 (15.58) [0]
1204	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	8/2016	9/2019 (3/2020) [9/2019]	1,388.34 (2,525.80) [2,525.80]	1,449.00 (1,137.46) [0]
1205	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN	3/2017	3/2020 (-) [4/2020]	754.54 (-) [756.27]	159.58 (1.73) [1]

1206	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS	12/2015	/ (9/2019) [0/0]	766.36 (-) [766.36]	666.72 (0.00) [0]
1207	FOUR LANING OF CHANDIGARH - KHARAR	10/2015	12/2017 (6/2020) [12/2019]	447.29 (746.43) [746.43]	600.33 (299.14) [24]
1208	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB	2/2018	/ (-) [1/2021]	261.76 (-) [207.00]	62.85 (-54.76) [-]
1209	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION	9/2014	/ (-) [3/2020]	479.00 (-) [479.00]	453.59 (0.00) [-]
1210	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200	10/2017	10/2019 (-) [10/2019]	1,069.59 (-) [1,069.59]	629.87 (0.00) [0]
1211	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI	3/2018	/ (-) [1/2020]	196.05 (149.90) [196.05]	143.03 (0.00) [-]
1212	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN	3/2018	/ (-) [0/0]	199.90 (149.90) [199.90]	60.39 (0.00) [0]
1213	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000	3/2018	11/2020 (-) [11/2020]	170.57 (-) [170.57]	46.23 (0.00) [0]
1214	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF	3/2018	6/2020 (-) [6/2020]	173.24 (-) [173.24]	10.97 (0.00) [0]
1215	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH	3/2018	7/2020 (-) [7/2020]	322.48 (-) [322.48]	48.73 (0.00) [0]
1216	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES	3/2018	8/2020 (-) [8/2020]	293.64 (-) [293.64]	28.24 (0.00) [0]
1217	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES	3/2018	8/2020 (-) [8/2020]	293.64 (-) [293.64]	28.24 (0.00) [0]
1218	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA	3/2018	8/2020 (-) [8/2020]	293.10 (-) [293.10]	10.26 (0.00) [0]
1219	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA	6/2015	/ (-) [0/0]	892.17 (-) [892.17]	648.44 (0.00) [0]
	<u>Urban Development</u>				
1220	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	2/2014	5/2017 (-) [10/2019]	388.00 (-) [488.28]	437.01 (100.28) [29]
1221	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	1/2018	5/2020 (-) [1/2021]	430.00 (-) [430.00]	77.69 (0.00) [8]
1222	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	8/2016	4/2019 (-) [2/2020]	294.00 (-) [294.00]	203.32 (0.00) [10]
	<u>RAJASTHAN</u>				
	<u>Atomic Energy</u>				
1223	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016 (-) [12/2020]	12,320.00 (17,079.00) [17,079.00]	11,387.00 (4,759.00) [48]
	<u>Coal</u>				
1224	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	3/2015	12/2019 (-) [0/0]	513.63 (-) [513.63]	175.30 (0.00) [0]

1225	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	3/2015	9/2019 (-) [0/0]	522.45 (-) [522.45]	9.88 (0.00) [0]
	<u>Petroleum</u>				
1226	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II	11/2011	3/2013 (-) [0/0]	310.00 (-) [370.00]	17.84 (60.00) [0]
1227	LPG BP PROJECT JODHPUR	3/2018	/ (-) [3/2021]	229.80 (-) [229.80]	69.24 (0.00) [-]
	<u>Power</u>				
1228	TRAMMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN	7/2016	1/2019 (7/2019) [9/2019]	1,429.38 (-) [1,429.38]	1,045.19 (0.00) [8]
	<u>Railways</u>				
1229	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	5/2015	/ (-) [0/0]	873.71 (-) [1,980.21]	4.25 (1,106.50) [0]
1230	AJMER-BANGURGRAM	4/2011	11/2019 (-) [5/2020]	213.39 (-) [303.56]	262.32 (90.17) [6]
1231	AJMER-KOTA (NASIRABAD-JAUNDRI)	4/2013	/ (-) [0/0]	822.00 (-) [1,099.54]	0.00 (277.54) [0]
1232	ALWAR-BANDIKUI DOUBLING	4/2013	2/2019 (-) [5/2020]	242.09 (281.03) [410.00]	351.23 (167.91) [15]
1233	BANGURGRAM-GURIYA PATCH DOUBLING	4/2012	12/2019 (-) [6/2020]	246.08 (-) [348.55]	215.47 (102.47) [6]
1234	DAUSA-GANGAPUR CITY(NL),NWR	2/1997	2/2019 (-) [3/2021]	410.08 (780.98) [886.41]	525.78 (476.33) [25]
1235	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM)	8/2018	8/2022 (-) [9/2022]	808.85 (-) [808.85]	47.07 (0.00) [1]
1236	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR	4/2013	3/2020 (-) [6/2020]	420.18 (-) [420.18]	160.53 (0.00) [3]
1237	MULTI MODAL LOGISTICS PARK AT KATHUWAS	1/2011	3/2018 (-) [3/2020]	493.17 (-) [493.17]	439.80 (0.00) [24]
1238	PUSHKAR-MERTA	4/2013	/ (-) [0/0]	323.00 (-) [432.22]	0.00 (109.22) [0]
1239	THIYAT HAMIRA-SANU	4/2013	10/2018 (-) [10/2019]	236.93 (-) [294.90]	141.40 (57.97) [12]
	<u>Road Transport And Highways</u>				
1240	2 LANING WITH PS OF GULABPURA - UNIARA	10/2015	10/2017 (4/2018) [1/2020]	597.00 (-) [597.00]	587.64 (0.00) [27]
1241	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR	8/2016	1/2019 (-) [10/2019]	320.30 (-) [320.30]	237.81 (0.00) [9]
1242	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA	11/2012	8/2016 (-) [12/2019]	530.07 (-) [530.07]	556.02 (0.00) [40]
1243	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A	7/2016	/ (5/2017) [11/2019]	688.70 (881.00) [688.70]	701.76 (0.00) [-]

1244	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE-	12/2016	/ (-) [8/2020]	1,031.95 (-) [1,031.95]	367.00 (0.00) [-]
1245	ALWAR-NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN.	3/2019	/ (-) [0/0]	178.13 (-) [178.13]	5.90 (0.00) [0]
1246	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM	8/2014	4/2018 (-) [0/0]	822.90 (-) [822.90]	844.08 (0.00) [0]
1247	CITTORGARH-NEEMACH (4L) OF NH-79 AND NIMBAHARA PRATAPGARH (2L+PS) OF NH-113 UNDER PPP.	10/2012	10/2013 (-) [0/0]	511.21 (-) [511.21]	814.79 (0.00) [0]
1248	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM	3/2018	/ (-) [0/0]	1,158.35 (-) [1,158.35]	245.17 (0.00) [0]
1249	CONSTRUCTION OF 4 LANING BY CC PAVEMENT ON KOTA-DARAH OF NH-12 FROM 256/550 TO 289/550 UNDER EPC.	12/2015	10/2016 (-) [0/0]	621.43 (-) [621.43]	426.36 (0.00) [0]
1250	CONSTRUCTION OF NAGAU BYPASS FROM EXISTING KM 166/260 TO KM 180/500 OF NH-65 ON EPC MODE.	3/2016	9/2016 (-) [0/0]	155.77 (-) [155.77]	97.42 (0.00) [0]
1251	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709	11/2017	4/2018 (-) [0/0]	163.95 (-) [163.95]	62.36 (0.00) [0]
1252	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH.	2/2018	/ (-) [0/0]	716.76 (-) [716.76]	171.45 (0.00) [0]
1253	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA	2/2018	/ (-) [0/0]	741.86 (-) [741.86]	0.00 (0.00) [0]
1254	DEVELOPMENT AND OPERATION OF BIKANER-SURATGARH SECTION OF NH-15 BY 2L+PS IN THE STATE OF RAJASTHAN	3/2009	9/2013 (-) [0/0]	501.00 (671.54) [671.54]	659.98 (170.54) [0]
1255	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO	12/2017	/ (-) [12/2020]	1,308.73 (-) [1,308.73]	99.68 (0.00) [-]
1256	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM	6/2016	6/2019 (-) [11/2019]	763.23 (-) [763.23]	216.17 (0.00) [5]
1257	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM	6/2016	6/2019 (-) [9/2019]	649.00 (-) [649.00]	296.30 (0.00) [3]
1258	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540	10/2017	10/2017 (-) [11/2020]	964.17 (-) [964.17]	370.32 (0.00) [37]
1259	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	2/2008	10/2011 (-) [0/0]	1,673.70 (-) [1,673.70]	3,326.93 (0.00) [0]
1260	NAGAU-BIKANER OF NH-11 (2L+PS) UNDER PPP.	1/2012	1/2014 (-) [0/0]	378.07 (478.73) [478.73]	188.98 (100.66) [0]
1261	NETRA VILLAGE TO MANDORE SECTION OF NH-65 KM 267+500 TO 296+070 (4L) UNDER EPC.	10/2014	1/2015 (-) [0/0]	382.81 (-) [382.81]	333.60 (0.00) [0]
1262	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING	9/2012	10/2013 (-) [0/0]	511.00 (-) [511.00]	492.00 (0.00) [0]
1263	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A	9/2012	10/2013 (-) [0/0]	511.00 (-) [511.00]	2,323.04 (0.00) [0]
1264	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE	10/2013	5/2014	278.87	0.00

	WITH PAVED SHOULDERS		(-) [0/0]	(-) [278.87]	(0.00) [0]
1265	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O	1/1991	4/2014 (-) [0/0]	376.52 (-) [376.52]	0.00 (0.00) [0]
1266	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I	9/2016	/ (-) [12/2019]	1,100.19 (-) [1,100.19]	900.00 (0.00) [-]
1267	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (	9/2016	/ (-) [5/2020]	1,239.82 (-) [1,239.82]	1,280.27 (0.00) [-]
1268	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV	4/2017	4/2020 (-) [11/2019]	894.00 (-) [894.00]	730.00 (0.00) [-5]
1269	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR	9/2014	9/2016 (9/2014) [10/2019]	425.19 (-) [425.19]	276.40 (0.00) [37]
1270	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR	8/2015	/ (2/2016) [10/2019]	275.90 (-) [275.90]	257.52 (0.00) [-]
1271	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM	7/2016	10/2018 (-) [0/0]	331.46 (-) [331.46]	267.94 (0.00) [0]
1272	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU	6/2016	6/2019 (-) [9/2019]	637.18 (-) [637.18]	588.00 (0.00) [3]
1273	UP-GRADATION TO 2 LANE WITH PAVED SHOULDER FOR SECTION FROM KM 118.900 TO KM 156.955 BALOTRA TOSANDE	1/2017	7/2017 (-) [0/0]	163.54 (-) [163.54]	93.15 (0.00) [0]
1274	UP-GRADATION TO TWO LANE WITH PAVED SHOULDER FOR SECTION FROM KM 58.000 TO KM 91.600 (BALOTRA TO SAN	1/2017	11/2017 (-) [0/0]	179.32 (-) [179.32]	96.12 (0.00) [0]
1275	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE - DANTOUR-JA	3/2018	/ (-) [0/0]	874.25 (-) [874.25]	80.10 (0.00) [0]
1276	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM-	2/2018	6/2018 (-) [0/0]	370.30 (-) [370.30]	192.88 (0.00) [0]
1277	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION	2/2018	/ (-) [9/2020]	1,103.88 (-) [1,103.88]	267.65 (0.00) [-]
1278	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM-	2/2018	5/2018 (-) [0/0]	341.79 (-) [341.79]	107.02 (0.00) [0]
1279	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING	10/2014	1/2015 (-) [0/0]	257.09 (-) [257.09]	14.18 (0.00) [0]
1280	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24	2/2015	3/2015 (-) [0/0]	383.40 (-) [383.40]	224.68 (0.00) [0]
1281	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K	10/2014	1/2015 (-) [0/0]	269.22 (-) [269.22]	33.24 (0.00) [0]
1282	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH	12/2015	6/2018 (-) [0/0]	621.43 (-) [621.43]	387.00 (0.00) [0]
1283	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR	11/2017	4/2018 (-) [0/0]	187.82 (-) [187.82]	53.11 (0.00) [0]
	<u>Urban Development</u>				
1284	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR	5/2015	3/2017	189.00	0.00

	100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS		(-) [0/0]	(-) [189.00]	(0.00) [0]
1285	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	12/2016	7/2019 (12/2019) [2/2020]	549.31 (559.47) [559.47]	348.69 (10.16) [7]
	<u>SIKKIM</u>				
	<u>Railways</u>				
1286	SEVOK RANGPO, NEFR	4/2008	12/2015 (-) [0/0]	1,339.48 (-) [4,084.69]	285.46 (2,745.21) [0]
	<u>Road Transport And Highways</u>				
1287	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	1/2013	2/2013 (9/2017) [12/2019]	182.28 (269.14) [269.14]	185.49 (86.86) [82]
1288	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	4/2013	8/2013 (-) [12/2019]	151.59 (240.58) [151.59]	196.76 (0.00) [76]
1289	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM.	4/2013	8/2013 (-) [0/0]	166.27 (203.26) [166.27]	141.31 (0.00) [0]
1290	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	3/2017	/ (-) [0/0]	375.80 (-) [375.80]	77.39 (0.00) [0]
1291	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	11/2017	11/2017 (-) [0/0]	290.05 (-) [290.05]	33.95 (0.00) [0]
1292	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA	4/2017	11/2017 (-) [0/0]	318.42 (-) [318.42]	97.85 (0.00) [0]
1293	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	3/2018	6/2018 (-) [0/0]	264.84 (-) [264.84]	0.00 (0.00) [0]
1294	RHENOK-RORATHANG-PAKYONG ON NH 717A	4/2017	10/2017 (-) [0/0]	388.00 (-) [447.37]	103.82 (59.37) [0]
	<u>TAMIL NADU</u>				
	<u>Atomic Energy</u>				
1295	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	3/2013	11/2020 (-) [11/2023]	39,849.00 (-) [39,849.00]	15,706.00 (0.00) [36]
1296	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	9/2003	9/2010 (-) [10/2021]	3,492.00 (-) [6,840.00]	5,821.38 (3,348.00) [133]
	<u>Civil Aviation</u>				
1297	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	6/2018	2/2022 (-) [8/2022]	2,467.00 (-) [2,467.00]	213.17 (0.00) [6]
1298	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI	8/2018	10/2021 (-) [10/2021]	951.28 (-) [951.28]	71.55 (0.00) [0]
	<u>Coal</u>				
1299	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	4/2013	6/2015 (-) [0/0]	1,458.17 (-) [709.06]	454.23 (-749.11) [0]
1300	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	6/2011	12/2015 (-) [12/2019]	5,907.11 (7,080.41) [7,080.41]	6,730.63 (1,173.30) [48]
	<u>Mines</u>				
1301	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU	9/2017	6/2019 (-) [0/0]	166.62 (-) [166.62]	134.98 (0.00) [0]

	<u>Petroleum</u>				
1302	AUGMENTATION OF CTMPL	12/2016	6/2020 (-) [6/2020]	228.00 (-) [228.00]	15.40 (0.00) [0]
1303	BS-VI PROJECTS	9/2017	12/2019 (-) [12/2019]	1,858.00 (-) [1,858.00]	1,026.86 (0.00) [0]
1304	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	12/2017	10/2020 (-) [8/2021]	466.43 (-) [466.43]	30.95 (0.00) [10]
1305	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	5/2016	12/2018 (-) [2/2021]	4,497.00 (6,025.00) [6,025.00]	499.65 (1,528.00) [26]
1306	ENNORE-TRICHY-MADURAI LPG PIPELINE	5/2013	6/2020 (-) [6/2020]	711.00 (-) [711.00]	11.12 (0.00) [0]
1307	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	11/2015	3/2019 (5/2020) [5/2020]	650.82 (-) [650.82]	394.21 (0.00) [14]
1308	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	2/2017 (-) [10/2021]	678.00 (-) [678.00]	5.57 (0.00) [56]
1309	RE-LIQUIFIED NATURAL GAS	8/2017	8/2020 (-) [8/2020]	421.00 (-) [421.00]	137.46 (0.00) [0]
1310	RESID UPGRADATION PROJECT	3/2013	11/2015 (-) [0/0]	3,110.36 (-) [3,110.36]	2,915.00 (0.00) [0]
	<u>Power</u>				
1311	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	5/2005	11/2008 (-) [0/0]	1,779.29 (-) [2,187.32]	2,237.45 (408.03) [0]
1312	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY	5/2017	7/2019 (-) [12/2019]	186.17 (-) [186.17]	107.75 (0.00) [5]
	<u>Railways</u>				
1313	ATTIPPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING	2/1999	3/2018 (-) [0/0]	257.00 (257.00) [257.00]	268.31 (0.00) [0]
1314	ATTIPPATTU PUTTUR	4/2008	2/2019 (-) [0/0]	151.84 (-) [1,105.00]	3.34 (953.16) [0]
1315	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	4/2007	/ (-) [3/2020]	931.98 (-) [951.24]	724.96 (19.26) [-]
1316	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	4/1999	/ (-) [0/0]	198.68 (-) [556.64]	303.72 (357.96) [0]
1317	ERODE-PALANI	4/2008	/ (-) [0/0]	288.57 (-) [1,140.00]	1.63 (851.43) [0]
1318	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	4/2006	6/2013 (-) [0/0]	495.74 (-) [734.01]	445.91 (238.27) [0]
1319	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	2/2015	3/2020 (-) [6/2021]	760.00 (-) [1,182.31]	406.32 (422.31) [15]
1320	MADURAI-BODINAYAKKANUR	4/2008	/ (-) [3/2020]	164.41 (-) [450.00]	151.50 (285.59) [-]
1321	MANIYACHI - NAGERCOIL (102 KM) DOUBLING	2/2015	3/2022	1,700.00	167.73

			(-) [3/2022]	(-) [1,003.00]	(-697.00) [0]
1322	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	9/2007	2/2019 (-) [2/2020]	724.69 (-) [2,072.50]	1,386.59 (1,347.81) [12]
1323	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM	10/2013	4/2014 (-) [3/2020]	187.26 (-) [231.67]	108.34 (44.41) [71]
1324	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	4/2013	/ (-) [0/0]	839.00 (-) [1,500.00]	0.62 (661.00) [0]
1325	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	2/1996	3/2005 (-) [0/0]	268.87 (-) [950.00]	927.86 (681.13) [0]
1326	TIDIVANAM-NAGARI (NL)	9/2006	/ (-) [0/0]	582.83 (-) [2,300.00]	241.39 (1,717.17) [0]
1327	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	9/2006	/ (-) [0/0]	227.40 (-) [900.00]	62.50 (672.60) [0]
1328	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	9/1995	3/2020 (-) [3/2021]	303.98 (-) [980.00]	669.21 (676.02) [12]
1329	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM)	2/2017	3/2024 (-) [3/2026]	1,567.00 (-) [1,567.00]	0.00 (0.00) [24]
	<u>Road Transport And Highways</u>				
1330	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI	9/2011	8/2013 (-) [0/0]	485.00 (-) [485.00]	406.68 (0.00) [0]
1331	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM)	4/2012	4/2014 (-) [0/0]	624.00 (-) [624.00]	350.79 (0.00) [0]
1332	4-LANNING OF OTTANCHATRAM BYPASS	9/2017	9/2017 (-) [12/2019]	244.27 (-) [244.27]	141.45 (0.00) [27]
1333	4-LANNING OF STHIYATHOPU-CHOLOPURAM	9/2017	9/2017 (-) [8/2020]	1,227.87 (-) [1,227.87]	225.96 (0.00) [35]
1334	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT	3/2015	8/2015 (-) [0/0]	258.97 (-) [268.92]	0.00 (9.95) [0]
1335	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I-	11/2015	8/2015 (-) [0/0]	154.14 (-) [154.14]	0.00 (0.00) [0]
1336	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	6/2011	6/2013 (1/2019) [8/2020]	600.00 (-) [600.00]	329.92 (0.00) [86]
1337	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS	3/2018	/ (-) [4/2021]	1,016.92 (-) [1,071.00]	0.00 (54.08) [-]
1338	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120	5/2015	11/2017 (-) [7/2019]	1,387.11 (-) [1,387.11]	974.13 (0.00) [0]
1339	FOUR LANING OF MADURAI- CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICKULAM (7/300)	3/2018	/ (-) [11/2020]	628.71 (-) [628.71]	59.22 (0.00) [-]
1340	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N	3/2018	/ (-) [0/0]	2,065.96 (-) [2,169.00]	0.00 (103.04) [0]
1341	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON	2/2018	/	1,166.26	0.00

	NH-227 IN THE STATE OF TAMIL NADU		(-) [2/2021]	(-) [1,166.26]	(0.00) [-]
1342	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	3/2016	7/2016 (-) [5/2020]	641.17 (-) [641.17]	354.03 (0.00) [46]
1343	FOUR LANING OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3	3/2018	/ (-) [11/2020]	505.35 (-) [505.35]	36.14 (0.00) [-]
1344	FOUR LANNING OF CHOLOPURAM-THANJAVUR	8/2017	8/2017 (-) [9/2020]	1,176.37 (-) [1,176.37]	155.12 (0.00) [37]
1345	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH	2/2016	8/2018 (-) [3/2020]	707.82 (-) [707.82]	343.21 (0.00) [19]
1346	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DSIGN CHAINAGE KM 0.000 TO KM 65.	3/2017	3/2020 (-) [3/2020]	848.45 (-) [848.45]	73.46 (0.00) [0]
1347	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K	2/2016	7/2018 (-) [5/2020]	641.17 (-) [641.17]	354.03 (0.00) [22]
1348	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO	3/2015	7/2015 (-) [0/0]	157.18 (162.00) [162.00]	0.00 (4.82) [0]
1349	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE	12/2017	/ (-) [3/2020]	379.90 (-) [379.90]	100.76 (0.00) [-]
1350	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	9/2011	12/2013 (-) [6/2020]	1,250.00 (-) [1,250.00]	1,333.68 (0.00) [78]
1351	THIRUMAYAM - MANAMADURAI SECTION	7/2014	1/2017 (-) [0/0]	401.11 (-) [401.11]	273.89 (0.00) [0]
1352	TRICHY - KARUR	3/2007	7/2008 (-) [0/0]	516.00 (-) [516.00]	936.30 (0.00) [0]
1353	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS	5/2010	5/2013 (-) [0/0]	374.00 (-) [374.00]	237.00 (0.00) [0]
1354	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N	3/2018	/ (-) [0/0]	633.55 (-) [482.04]	0.00 (-151.51) [0]
1355	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	6/2015	12/2017 (-) [0/0]	563.92 (-) [563.92]	93.53 (0.00) [0]
	<u>Urban Development</u>				
1356	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	12/2015	10/2019 (-) [3/2020]	209.00 (-) [209.00]	130.62 (0.00) [5]
1357	CHENNAI METRO RAIL LTD (PHASE 1 EXT)	6/2016	3/2018 (-) [0/0]	3,770.00 (-) [3,770.00]	0.00 (0.00) [0]
1358	CHENNAI METRO RAIL LTD (PHASE 1)	2/2009	12/2015 (-) [0/0]	14,600.00 (-) [19,058.00]	16,352.87 (4,458.00) [0]
1359	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI	11/2017	/ (-) [11/2021]	348.77 (-) [348.77]	14.52 (0.00) [-]
	<u>TELANGANA</u>				
	<u>Coal</u>				
1360	KALYANIKHANI 6 INCLINE PROJECT	12/2015	3/2020 (-)	477.65 (-)	2.11 (0.00)

			[3/2020]	[477.65]	[0]
1361	KOYAGUDEM OPENCAST PROJECT	10/2015	3/2018 (-) [3/2020]	426.79 (-) [426.79]	0.72 (0.00) [24]
1362	JALAGAM VENGALA RAO OCP-II	7/2011	3/2015 (-) [3/2021]	447.06 (-) [473.22]	18.35 (26.16) [72]
1363	KAKATIYA LONGWALL	12/2008	12/2012 (-) [0/0]	453.63 (-) [453.63]	121.91 (0.00) [0]
1364	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1	3/2017	3/2019 (-) [3/2022]	413.84 (-) [413.84]	54.51 (0.00) [36]
1365	KAKATIYAKHANI OPENCAST-2 PROJECT	5/2015	3/2019 (-) [3/2020]	397.09 (-) [442.42]	92.46 (45.33) [12]
1366	KALYANIKHANI OPENCAST PROJECT	7/2012	7/2016 (-) [3/2020]	417.33 (-) [384.32]	103.95 (-33.01) [44]
1367	KISTARAM OCP	11/2010	3/2015 (-) [3/2021]	242.29 (-) [164.04]	119.59 (-78.25) [72]
1368	MANUGURU OC-II EXTENSION PHASE-II	3/2010	3/2012 (-) [0/0]	181.19 (-) [181.19]	170.60 (0.00) [0]
1369	RAMAGUNDAM OC-II EXTENSION	12/2009	3/2012 (-) [3/2023]	418.97 (-) [489.62]	343.10 (70.65) [132]
1370	RAMPURAM SHAFT BLOCK	8/2016	/ (3/2023) [0/0]	431.92 (-) [431.92]	0.00 (0.00) [0]
1371	RCE OF INDARAM OCP(1.20 MTPA)	7/2011	3/2015 (-) [3/2021]	162.76 (-) [349.28]	8.00 (186.52) [72]
1372	RFR OF MANUGURU OC PROJECT	11/2012	3/2016 (-) [3/2020]	430.45 (-) [415.37]	166.43 (-15.08) [48]
1373	RG OC -III EXTENSION (PHASE -II) PROJECT	6/2012	6/2015 (-) [3/2020]	365.01 (-) [365.01]	135.62 (0.00) [57]
1374	RKP OCP PHASE-I	3/2010	3/2015 (-) [3/2020]	209.78 (-) [209.78]	154.58 (0.00) [60]
1375	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	3/2012 (-) [3/2024]	249.03 (-) [448.86]	286.19 (199.83) [144]
1376	SRAVANAPALLI OPENCAST PROJECT	2/2018	/ (3/2023) [0/0]	412.70 (-) [412.70]	0.11 (0.00) [0]
1377	SRP OC-II EXPANSION PROJECT	11/2016	/ (4/2017) [3/2020]	272.73 (-) [272.73]	162.62 (0.00) [-]
	<u>Petroleum</u>				
1378	GRASS ROOT TERMINAL AT MALKAPUR	12/2018	4/2022 (-) [4/2022]	611.00 (-) [611.00]	1.68 (0.00) [0]
	<u>Power</u>				
1379	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	1/2016	11/2020 (6/2021) [6/2021]	10,598.98 (-) [10,598.98]	5,557.96 (0.00) [7]
	<u>Railways</u>				

1380	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	4/2012	3/2016 (-) [12/2020]	632.68 (-) [816.55]	686.11 (183.87) [57]
1381	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY	3/2015	3/2021 (-) [3/2021]	636.38 (-) [636.38]	281.85 (0.00) [0]
1382	KONDAPALLI-KOTHAGUDEM	4/2013	/ (-) [0/0]	723.00 (-) [997.09]	0.00 (274.09) [0]
1383	MACHERLA-NALGONDA(NL)(SCR)	7/1998	/ (-) [0/0]	458.25 (-) [458.26]	3.83 (0.01) [0]
1384	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	4/2017	3/2022 (-) [3/2022]	119.73 (185.00) [184.97]	3.67 (65.24) [0]
1385	MANOHARABAD-KOTHPALL NEW LINE(SCR)	4/2006	3/2010 (-) [3/2023]	1,160.48 (-) [1,160.48]	288.38 (0.00) [156]
1386	MANUGURU-RAMAGUNDAM	4/2013	/ (-) [0/0]	1,112.00 (-) [2,911.84]	0.92 (1,799.84) [0]
1387	SECUNDERABAD-MAHABUBNAGAR DOUBLING	4/2015	12/2024 (-) [12/2024]	773.94 (-) [773.94]	413.71 (0.00) [0]
	<u>Road Transport And Highways</u>				
1388	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	4/2014	9/2016 (-) [9/2019]	1,266.60 (1,544.00) [1,544.00]	1,446.45 (277.40) [36]
1389	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH	1/2018	5/2020 (-) [5/2020]	283.15 (-) [283.15]	42.22 (0.00) [0]
1390	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES	3/2018	7/2020 (-) [7/2020]	626.76 (-) [626.76]	80.66 (0.00) [0]
1391	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM	3/2015	1/2017 (-) [9/2019]	153.21 (-) [153.21]	100.10 (0.00) [32]
1392	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB	3/2017	3/2017 (-) [0/0]	4,429.00 (-) [4,429.00]	0.00 (0.00) [0]
1393	FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3	3/2018	/ (-) [0/0]	857.62 (-) [857.62]	0.03 (0.00) [0]
1394	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K	3/2018	/ (-) [0/0]	802.65 (-) [802.65]	80.29 (0.00) [0]
1395	FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM	3/2018	/ (-) [0/0]	950.63 (-) [950.63]	62.00 (0.00) [0]
1396	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT	3/2018	/ (-) [0/0]	828.29 (-) [828.29]	0.00 (0.00) [0]
1397	FOUR LANING OF YADGIRI - WARANGAL	12/2015	11/2018 (7/2019) [12/2019]	1,423.96 (897.03) [897.03]	737.19 (-526.93) [13]
1398	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365	3/2018	7/2019 (-) [12/2019]	192.67 (-) [192.67]	107.37 (0.00) [5]
1399	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR	1/2017	10/2019 (-) [10/2019]	605.08 (-) [605.08]	273.88 (0.00) [0]

1400	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN	2/2018	4/2020 (-) [4/2020]	426.52 (-) [426.52]	225.51 (0.00) [0]
1401	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT	1/2014	3/2016 (-) [0/0]	270.00 (-) [270.00]	19.84 (0.00) [0]
1402	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT	2/2018	11/2019 (-) [11/2019]	294.13 (-) [294.13]	39.44 (0.00) [0]
1403	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS	2/2018	11/2019 (-) [11/2019]	220.28 (-) [220.28]	37.58 (0.00) [0]
1404	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC	3/2018	9/2020 (-) [9/2020]	322.81 (-) [322.81]	1.66 (0.00) [0]
1405	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ	10/2016	3/2019 (-) [12/2019]	248.83 (-) [248.83]	88.85 (0.00) [9]
1406	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON	10/2016	2/2019 (-) [12/2019]	298.32 (-) [298.32]	77.44 (0.00) [10]
1407	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4	1/2018	12/2019 (-) [12/2019]	230.03 (-) [230.03]	127.98 (0.00) [0]
1408	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59	2/2018	6/2020 (-) [6/2020]	206.13 (-) [206.13]	127.86 (0.00) [0]
1409	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR	1/2019	/ (-) [0/0]	193.19 (-) [193.19]	0.00 (0.00) [0]
1410	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON- THIRUMALAGIRI OF NH	1/2017	10/2019 (-) [10/2019]	196.52 (-) [196.52]	103.12 (0.00) [0]
1411	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA- KALWAKURTHY SECTI	1/2017	12/2019 (-) [12/2019]	283.00 (-) [283.00]	152.35 (0.00) [0]
1412	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE	1/2017	5/2019 (9/2019) [0/0]	244.54 (-) [244.54]	137.63 (0.00) [0]
1413	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA- RAVULAPALLY SECT	1/2017	5/2019 (-) [8/2019]	359.27 (-) [359.27]	228.00 (0.00) [0]
1414	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY- MALLEPALLY SECTION	1/2017	5/2019 (-) [12/2019]	300.00 (-) [300.00]	99.46 (0.00) [7]
	<u>Urban Development</u>				
1415	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD	10/2016	3/2020 (-) [5/2021]	209.84 (-) [209.84]	35.79 (0.00) [14]
	<u>TRIPURA</u>				
	<u>Civil Aviation</u>				
1416	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	9/2015	6/2019 (-) [12/2019]	338.93 (-) [339.00]	213.50 (0.07) [6]
	<u>Railways</u>				
1417	AGARTALA-AKHAURA NL	4/2012	3/2020 (-) [12/2021]	569.63 (-) [650.00]	45.24 (80.37) [21]
	<u>Road Transport And Highways</u>				
1418	2 LANING WITH PAVED SHOULDER OF AGARTALA- UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM	10/2014	3/2018 (12/2019)	369.00 (-)	308.97 (0.00)

	55.00 IN THE S		[12/2019]	[369.00]	[21]
1419	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C	10/2016	8/2020 (-) [8/2020]	171.90 (-) [171.90]	11.75 (0.00) [0]
	<u>Urban Development</u>				
1420	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	3/2007	12/2015 (-) [0/0]	149.73 (173.00) [175.94]	178.65 (26.21) [0]
1421	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016 (-) [0/0]	202.61 (227.00) [227.00]	199.95 (24.39) [0]
1422	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	12/2016 (-) [0/0]	175.49 (206.71) [206.71]	141.28 (31.22) [0]
	<u>UTTAR PRADESH</u>				
	<u>Civil Aviation</u>				
1423	CCS INTERNATIONAL AIRPORT , LUCKNOW	6/2018	9/2021 (-) [9/2021]	1,383.00 (-) [1,383.00]	210.62 (0.00) [0]
	<u>Coal</u>				
1424	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	7/2016	11/2021 (-) [11/2021]	17,237.00 (-) [17,237.80]	7,532.67 (0.80) [0]
	<u>Health And Family Welfare</u>				
1425	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	7/2016	4/2020 (-) [6/2020]	785.00 (-) [785.00]	244.66 (0.00) [2]
1426	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI	3/2018	/ (-) [4/2020]	268.84 (-) [268.84]	99.26 (0.00) [-]
	<u>Petroleum</u>				
1427	120 TMTA LPG BOTTLING PLANT AT GORAKHPUR UP	3/2014	9/2019 (-) [9/2019]	204.00 (-) [204.00]	139.25 (0.00) [0]
1428	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A	3/2018	12/2021 (-) [12/2021]	676.00 (-) [676.00]	168.18 (0.00) [0]
1429	BS-VI PROJECT AT MATHURA REFINERY	1/2018	9/2019 (-) [1/2020]	666.64 (-) [666.64]	431.71 (0.00) [4]
1430	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI	4/2017	4/2022 (-) [4/2022]	287.49 (-) [287.49]	125.82 (0.00) [0]
1431	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY	8/2017	8/2020 (-) [8/2020]	255.40 (-) [255.40]	1.75 (0.00) [0]
1432	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL	12/2017	12/2021 (-) [12/2021]	1,524.06 (-) [1,524.06]	13.73 (0.00) [0]
1433	REDEVELOPMENT/ EXPANSION OF MEERUT DEPOT FOR ENHANCING PRODUCT HANDLING CAPACITY	8/2016	11/2019 (-) [11/2019]	154.84 (-) [154.84]	120.67 (0.00) [0]
1434	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR	8/2017	8/2021 (-) [11/2021]	318.80 (-) [318.80]	40.06 (0.00) [3]
	<u>Power</u>				
1435	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP	12/2018	9/2020 (-) [9/2020]	587.44 (-) [587.44]	250.00 (0.00) [0]
1436	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP	3/2019	11/2020 (-)	349.00 (-)	125.00 (0.00)

			[11/2020]	[349.00]	[0]
1437	DHUKWAN SMALL HYDRO PROJECT	5/2011	2/2014 (-) [12/2019]	195.42 (-) [294.60]	310.08 (99.18) [70]
1438	KHURJA SUPER THERMAL POWER PROJECT	3/2019	9/2023 (-) [9/2023]	11,089.42 (-) [11,089.42]	521.82 (0.00) [0]
1439	MUNPL-MEJA TPP - JV (2X660 MW)	4/2012	2/2017 (6/2020) [6/2020]	9,750.89 (-) [12,176.28]	9,794.00 (2,425.39) [40]
1440	TANDA TPP STAGE-II (2X660 MW)	9/2014	7/2019 (3/2020) [7/2020]	9,188.98 (-) [9,188.98]	6,502.04 (0.00) [12]
	<u>Railways</u>				
1441	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP	3/2013	/ (-) [0/0]	307.00 (-) [1,409.09]	0.00 (1,102.09) [0]
1442	AUNRIHAR - JAUNPUR PATCH DOUBLING .	4/2016	1/2022 (-) [1/2022]	600.00 (-) [600.00]	25.24 (0.00) [0]
1443	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI.	4/2016	1/2022 (-) [1/2022]	1,900.00 (-) [1,277.06]	0.00 (-622.94) [0]
1444	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	3/2012	12/2020 (-) [12/2022]	1,183.25 (-) [1,183.25]	1,072.44 (0.00) [24]
1445	BURHWAL - GONDA - 3RD RUNNING LINE.	4/2016	/ (-) [0/0]	602.50 (-) [714.34]	17.35 (111.84) [0]
1446	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	2/2008	3/2012 (-) [0/0]	171.10 (-) [275.08]	141.55 (103.98) [0]
1447	ETAH - KASGANJ - NEW LINE	4/2017	4/2017 (-) [4/2022]	276.90 (-) [276.90]	0.00 (0.00) [60]
1448	ETAWAH-MAINPURI (NL),NCR	4/1997	12/2008 (-) [0/0]	120.00 (-) [346.00]	345.51 (226.00) [0]
1449	GHAZIPUR - AUNRIHAR (40 KM)	4/2014	/ (-) [0/0]	182.92 (-) [197.73]	0.00 (14.81) [0]
1450	INDARA - DOHRIGHAT GAUGE CONVERSION.	4/2016	4/2016 (-) [6/2020]	213.00 (-) [213.35]	8.97 (0.35) [50]
1451	JHANSI BINA DOUBLING	9/2016	3/2021 (-) [3/2021]	2,001.00 (-) [2,001.00]	416.59 (0.00) [0]
1452	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING	3/2018	3/2023 (-) [3/2023]	4,329.53 (-) [4,329.53]	3.90 (0.00) [0]
1453	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP	3/2013	/ (-) [0/0]	643.00 (-) [644.00]	0.00 (1.00) [0]
1454	KARAILA ROAD - SHAKTINAGAR DOUBLING	8/2015	3/2019 (-) [12/2019]	528.57 (-) [528.57]	107.81 (0.00) [9]
1455	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	4/2011	3/2019 (-) [3/2020]	927.01 (-) [1,200.00]	1,147.34 (272.99) [12]
1456	MATHURA-PLWAL 4TH LINE (80KM)	4/2015	3/2020 (-)	668.70 (668.00)	330.00 (11.30)

			[3/2020]	[680.00]	[0]
1457	MAU-GHAZIPUR-TARIGHAT NEW LINE	4/2015	3/2023 (-) [12/2024]	1,765.92 (-) [1,765.92]	601.87 (0.00) [21]
1458	NANPARA - NEPALGANJ GAUGE CONVERSION.	4/2017	4/2017 (-) [10/2022]	150.00 (-) [150.00]	0.00 (0.00) [66]
1459	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE	4/2017	1/2018 (-) [0/0]	1,343.00 (-) [1,476.15]	0.00 (133.15) [0]
1460	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION	4/2017	4/2017 (-) [1/2020]	622.50 (427.00) [426.74]	179.51 (-195.76) [33]
1461	RAMNA - SINGRAULI DOUBLING	8/2015	3/2020 (-) [3/2021]	2,436.21 (-) [2,436.21]	517.46 (0.00) [12]
1462	ROSA-SITAPUR CANTT-BURHWAL DOUBLING	3/2015	3/2022 (-) [12/2019]	1,295.42 (-) [1,295.42]	328.56 (0.00) [-27]
1463	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING.	4/2016	12/2019 (-) [4/2021]	1,177.96 (-) [1,028.95]	26.06 (-149.01) [16]
1464	UNCHA HAR-AMETHI	4/2012	/ (-) [3/2023]	1,229.00 (-) [1,230.00]	103.17 (1.00) [-]
1465	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	4/2015	3/2022 (-) [12/2024]	943.60 (-) [750.56]	372.23 (-193.04) [33]
	Road Transport And Highways				
1466	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125	9/2015	9/2016 (3/2018) [3/2018]	368.73 (-) [368.73]	236.49 (0.00) [0]
1467	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE	11/2010	3/2017 (-) [0/0]	305.49 (-) [305.49]	131.08 (0.00) [0]
1468	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232	4/2014	1/2016 (-) [0/0]	351.34 (-) [351.34]	433.68 (0.00) [0]
1469	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI	4/2014	1/2016 (-) [0/0]	495.78 (-) [495.78]	633.24 (0.00) [0]
1470	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	7/2012	1/2014 (-) [0/0]	291.36 (-) [291.36]	459.07 (0.00) [0]
1471	2-LANING WITH PS SITARGANJ BAREILY SECTION	6/2014	1/2016 (-) [0/0]	301.04 (-) [301.04]	207.94 (0.00) [0]
1472	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500	8/2016	4/2019 (11/2019) [11/2019]	2,016.00 (-) [2,016.00]	1,996.00 (0.00) [7]
1473	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C	3/2018	/ (-) [0/0]	1,120.57 (-) [1,120.57]	0.00 (0.00) [0]
1474	4-LANING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (	3/2016	/ (-) [1/2020]	1,668.00 (-) [1,668.00]	946.08 (0.00) [-]
1475	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I)	12/2015	6/2016 (-) [0/0]	611.65 (-) [611.65]	728.24 (0.00) [0]
1476	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00	3/2016	/ (-)	1,408.00 (-)	442.70 (0.00)

			[7/2020]	[1,408.00]	[-]
1477	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00	3/2016	/ (-) [4/2020]	1,737.00 (-) [1,737.00]	1,159.07 (0.00) [-]
1478	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR)	3/2016	/ (-) [0/0]	1,404.50 (-) [1,404.50]	92.37 (0.00) [0]
1479	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 TO 208.300 KM [PACKAGE-IV]	3/2016	4/2019 (10/2019) [10/2019]	1,587.49 (-) [2,982.00]	276.87 (1,394.51) [6]
1480	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 TO 148.00 KM 4-LANNING OF VARANASI GORAKHPUR	3/2016	/ (-) [0/0]	1,396.74 (-) [1,396.74]	227.26 (0.00) [0]
1481	6 LANING OF AGRA - ETAWAH BYPASS	7/2015	1/2019 (-) [0/0]	1,657.20 (-) [1,657.20]	2,345.00 (0.00) [0]
1482	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	3/2017	3/2020 (-) [3/2020]	2,064.99 (-) [2,447.00]	1,653.62 (382.01) [0]
1483	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN	12/2017	/ (-) [0/0]	207.00 (-) [207.00]	0.00 (0.00) [0]
1484	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020	3/2016	4/2019 (-) [0/0]	676.73 (-) [676.73]	632.21 (0.00) [0]
1485	BAREILY-SITAPUR (NH-24)	3/2011	9/2013 (-) [0/0]	1,046.00 (-) [1,046.00]	805.19 (0.00) [0]
1486	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA	2/2018	/ (2/2019) [2/2022]	972.77 (1,444.25) [972.77]	0.00 (0.00) [-]
1487	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T	12/2016	/ (-) [9/2019]	534.55 (-) [531.00]	433.62 (-3.55) [-]
1488	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O	12/2017	/ (-) [0/0]	305.00 (-) [305.00]	0.00 (0.00) [0]
1489	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO	3/2018	/ (12/2018) [12/2021]	1,117.84 (1,684.93) [1,117.84]	0.00 (0.00) [-]
1490	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650	1/2017	/ (-) [0/0]	450.68 (-) [450.68]	397.62 (0.00) [0]
1491	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B	1/2014	3/2016 (-) [0/0]	282.41 (-) [282.41]	155.53 (0.00) [0]
1492	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM	1/2016	6/2019 (12/2016) [9/2019]	1,081.57 (1,240.03) [1,057.60]	1,000.89 (-23.97) [3]
1493	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM	12/2017	/ (2/2018) [3/2020]	1,232.21 (3,207.63) [1,087.00]	473.11 (-145.21) [-]
1494	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO	3/2017	3/2020 (11/2017) [5/2020]	1,989.00 (2,602.09) [1,989.00]	852.57 (0.00) [2]
1495	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II)	9/2015	3/2018 (-) [0/0]	785.78 (-) [785.78]	902.00 (0.00) [0]
1496	ETAWAH CHAKERI	3/2013	9/2015 (-) [0/0]	1,573.00 (-) [1,573.00]	1,998.25 (0.00) [0]

1497	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP	2/2018	/ (-) [0/0]	670.50 (-) [670.50]	0.00 (0.00) [0]
1498	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS	3/2018	/ (-) [0/0]	809.07 (-) [809.07]	0.00 (0.00) [0]
1499	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR.	3/2018	/ (-) [0/0]	925.40 (-) [925.40]	0.00 (0.00) [0]
1500	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II)	12/2015	6/2018 (-) [4/2020]	667.00 (3,007.86) [667.00]	549.07 (0.00) [22]
1501	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III)	6/2016	7/2018 (-) [4/2020]	667.00 (2,257.49) [667.00]	464.05 (0.00) [21]
1502	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I)	1/2016	6/2018 (-) [6/2020]	1,027.53 (2,433.38) [1,027.53]	601.13 (0.00) [24]
1503	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II)	1/2016	6/2018 (-) [6/2020]	815.28 (2,182.03) [815.28]	520.89 (0.00) [24]
1504	FOUR LANING OF VARANASI BYPASS	5/2015	5/2017 (-) [0/0]	261.09 (275.00) [261.09]	240.96 (0.00) [0]
1505	FOUR LANING WIDENING & STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONALI - GORAKHPUR ROAD (JAN	3/2018	8/2020 (-) [8/2020]	288.30 (-) [288.30]	0.34 (0.00) [0]
1506	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2	3/2017	3/2020 (-) [11/2020]	1,373.28 (-) [1,373.28]	571.96 (0.00) [8]
1507	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	3/2017	3/2020 (-) [8/2020]	1,184.71 (-) [1,310.00]	563.15 (125.29) [5]
1508	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791	3/2016	4/2019 (7/2020) [7/2020]	899.00 (-) [899.00]	532.53 (0.00) [15]
1509	GHAZIABAD-ALIGARH NH-91	2/2011	8/2013 (-) [0/0]	1,141.00 (-) [1,141.00]	1,715.42 (0.00) [0]
1510	IMPROVEMENT AND UP-GRADATION OF EXISITING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T	11/2018	/ (-) [0/0]	281.45 (-) [281.45]	0.00 (0.00) [0]
1511	MEERUT-BULANDSHAHR	1/2016	/ (-) [0/0]	683.24 (-) [683.24]	623.53 (0.00) [0]
1512	R AND U FROM KM 385.00 TO KM 420.000 TO 2- LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404	12/2016	10/2019 (-) [10/2019]	209.10 (-) [209.10]	54.18 (0.00) [0]
1513	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS	11/2016	/ (-) [0/0]	326.99 (327.00) [326.99]	0.00 (0.00) [0]
1514	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS	3/2016	9/2020 (-) [9/2020]	296.50 (-) [296.50]	0.51 (0.00) [0]
1515	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU	3/2018	/ (-) [0/0]	1,025.80 (-) [677.07]	115.83 (-348.73) [0]
1516	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA	3/2018	/ (-) [0/0]	1,115.28 (-) [770.04]	216.33 (-345.24) [0]
1517	REHABILITATION AND UPGRADATION OF ALLAHABAD -	10/2016	2/2019	239.63	211.57

	MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2-		(-) [7/2019]	(-) [239.63]	(0.00) [0]
1518	REHABILITATION AND UPGRADATION OF BARAICH - SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA	3/2016	12/2019 (-) [12/2019]	388.83 (-) [388.83]	280.17 (0.00) [0]
1519	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750	3/2018	4/2020 (-) [4/2020]	263.89 (-) [263.89]	67.69 (0.00) [0]
1520	REHABILITATION AND UPGRADATION OF HARPALPUR - SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE	3/2016	11/2019 (-) [11/2019]	208.50 (-) [208.50]	123.66 (0.00) [0]
1521	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH	10/2013	3/2017 (-) [9/2019]	445.89 (653.00) [653.29]	464.05 (207.40) [30]
1522	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F	3/2016	1/2020 (-) [1/2020]	599.34 (-) [599.34]	449.19 (0.00) [0]
1523	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF	3/2018	2/2020 (-) [2/2020]	185.18 (-) [185.18]	2.86 (0.00) [0]
1524	REHABILITATION AND UPGRADATION OF TULSIPUR - BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730	3/2016	5/2019 (-) [11/2019]	249.50 (-) [249.50]	150.70 (0.00) [6]
1525	REHABILITATION AND UPGRADATION OF ALLAHABAD - MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT	10/2016	3/2020 (-) [3/2020]	218.90 (-) [218.90]	23.37 (0.00) [0]
1526	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230	3/2018	/ (-) [0/0]	306.59 (-) [306.59]	0.00 (0.00) [0]
1527	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P	11/2016	9/2019 (-) [9/2019]	215.16 (215.00) [215.16]	157.79 (0.00) [0]
1528	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH	3/2016	1/2020 (-) [1/2020]	240.30 (240.00) [240.30]	194.01 (0.00) [0]
1529	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA	10/2016	3/2020 (-) [3/2020]	218.94 (219.00) [218.94]	86.07 (0.00) [0]
1530	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO	10/2016	10/2018 (-) [9/2019]	176.94 (177.00) [176.94]	132.45 (0.00) [11]
1531	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO	7/2016	10/2019 (-) [10/2019]	208.88 (-) [208.88]	36.25 (0.00) [0]
1532	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270	10/2013	3/2017 (-) [9/2019]	445.89 (-) [653.29]	464.05 (207.40) [30]
1533	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14	11/2017	1/2019 (-) [0/0]	2,159.00 (-) [2,159.00]	715.78 (0.00) [0]
1534	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA	3/2018	/ (-) [0/0]	2,140.93 (-) [2,140.93]	0.00 (0.00) [0]
1535	VARANASI RING ROAD PKG - I	1/2018	/ (-) [0/0]	450.77 (929.89) [450.77]	0.00 (0.00) [0]
1536	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH	5/2013	8/2015 (-) [9/2019]	164.54 (165.00) [164.54]	89.14 (0.00) [49]
1537	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE	5/2013	8/2015 (-)	164.54 (-)	89.14 (0.00)

			[9/2019]	[164.54]	[49]
	<u>Steel</u>				
1538	FORGED WHEEL PLANT	4/2014	9/2018 (10/2019) [10/2019]	1,682.85 (-) [1,682.85]	1,227.53 (0.00) [13]
	<u>Urban Development</u>				
1539	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR	11/2017	3/2020 (-) [3/2020]	171.72 (-) [171.72]	32.00 (0.00) [0]
1540	LUCKNOW METRO RAIL CORPORATION LTD	1/2016	3/2019 (-) [0/0]	6,928.00 (6,928.00) [6,928.00]	2,536.77 (0.00) [0]
	<u>UTTARAKHAND</u>				
	<u>Civil Aviation</u>				
1541	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN	7/2018	9/2020 (-) [9/2020]	353.27 (-) [353.27]	114.29 (0.00) [0]
	<u>Petroleum</u>				
1542	SITARGANJ LPG PROJECT	2/2017	2/2020 (-) [10/2020]	160.10 (-) [160.10]	41.22 (0.00) [8]
	<u>Power</u>				
1543	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	7/2012	8/2017 (-) [0/0]	1,527.00 (-) [1,801.07]	148.93 (274.07) [0]
1544	NAITWAR MORI HEP	10/2017	12/2021 (-) [12/2021]	648.33 (-) [648.33]	265.90 (0.00) [0]
1545	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	3/2013 (12/2020) [1/2021]	2,978.48 (5,867.38) [5,867.38]	4,182.37 (2,888.90) [94]
1546	TEHRI PUMPED STORAGE PLANT(1000MW)	7/2006	2/2016 (-) [6/2022]	1,657.00 (-) [5,024.35]	3,047.08 (3,367.35) [76]
1547	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	8/2008	6/2013 (-) [12/2022]	2,491.58 (-) [4,397.80]	1,770.91 (1,906.22) [114]
	<u>Railways</u>				
1548	HARIDWAR-LAKSAR	4/2012	/ (-) [6/2020]	219.83 (-) [346.63]	229.48 (126.80) [-]
1549	KICHHA-KHATIMA (NL) - NER	4/2003	/ (-) [0/0]	142.45 (-) [228.40]	0.15 (85.95) [0]
1550	RISHIKESH - KARNAPRAYAG NEW LINE	4/2011	12/2024 (-) [3/2025]	16,216.00 (-) [16,216.00]	1,655.10 (0.00) [3]
	<u>Road Transport And Highways</u>				
1551	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI	3/2018	6/2018 (-) [0/0]	403.36 (-) [403.36]	89.19 (0.00) [0]
1552	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA	3/2018	5/2018 (-) [0/0]	417.24 (-) [417.24]	87.71 (0.00) [0]
1553	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	11/2012	7/2018 (12/2019) [2/2020]	605.84 (-) [722.46]	722.46 (116.62) [19]
1554	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900	3/2016	/ (-) [2/2020]	1,443.00 (-) [1,443.00]	1,246.85 (0.00) [-]
1555	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD	3/2018	5/2018	274.31	19.22

	TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399		(-) [0/0]	(-) [274.31]	(0.00) [0]
1556	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK)	3/2018	7/2018 (-) [0/0]	1,383.78 (-) [1,383.78]	107.45 (0.00) [0]
1557	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN	5/2018	5/2020 (-) [5/2020]	248.00 (-) [248.00]	0.00 (0.00) [0]
1558	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88	3/2016	/ (10/2020) [10/2020]	720.00 (-) [720.00]	285.96 (0.00) [-]
1559	HARIDWAR DEHRADUN APPROVED LENGTH 69	11/2011	10/2013 (-) [2/2020]	478.51 (-) [478.00]	315.11 (-0.51) [76]
1560	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG	11/2017	11/2019 (-) [11/2019]	232.81 (-) [232.81]	59.44 (0.00) [0]
1561	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION	11/2017	11/2019 (-) [11/2019]	283.51 (-) [283.51]	126.38 (0.00) [0]
1562	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	12/2017	12/2019 (-) [12/2019]	257.34 (-) [257.34]	62.79 (0.00) [0]
1563	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	6/2017	6/2019 (-) [12/2019]	282.08 (-) [282.08]	77.05 (0.00) [6]
1564	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	12/2017	12/2019 (-) [12/2019]	200.34 (-) [200.34]	31.00 (0.00) [0]
1565	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR	2/2018	2/2020 (-) [2/2020]	418.88 (-) [418.88]	88.00 (0.00) [0]
1566	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	11/2017	11/2019 (-) [11/2019]	266.52 (-) [266.52]	144.27 (0.00) [0]
1567	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER	8/2016	12/2017 (-) [12/2019]	234.88 (-) [208.89]	118.26 (-25.99) [24]
1568	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K	2/2018	/ (-) [0/0]	293.68 (-) [293.68]	11.57 (0.00) [0]
1569	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00	3/2018	/ (-) [0/0]	460.73 (-) [461.00]	0.00 (0.27) [0]
1570	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00	12/2017	12/2019 (-) [12/2019]	248.22 (-) [248.22]	57.20 (0.00) [0]
	<u>Urban Development</u>				
1571	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	12/2013 (-) [10/2019]	114.26 (266.00) [266.00]	0.00 (151.74) [70]
	<u>WEST BENGAL</u>				
	<u>Civil Aviation</u>				
1572	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA	1/2019	11/2021 (-) [11/2021]	264.99 (-) [264.99]	0.42 (0.00) [0]
1573	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA	1/2016	3/2020 (-) [12/2020]	219.91 (-) [219.91]	61.61 (0.00) [9]
	<u>Coal</u>				
1574	JHANJRA COMBINED PR(3.50 MTY)	11/2015	3/2022	602.86	315.69

			(-) [3/2022]	(-) [602.86]	(0.00) [0]
1575	NAKRAKONDA KUMARDIH B OCP	8/2018	3/2029 (-) [3/2029]	502.68 (-) [502.68]	0.00 (0.00) [0]
1576	RANIGANJ MASTER PLAN	8/2009	8/2019 (-) [0/0]	2,661.73 (-) [5,186.24]	330.94 (2,524.51) [0]
1577	SIDULI MINE (OC AND UG)	5/2018	3/2026 (-) [3/2026]	535.18 (-) [535.18]	0.00 (0.00) [0]
1578	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	8/2012	3/2018 (-) [10/2020]	1,055.05 (-) [1,055.05]	510.31 (0.00) [31]
1579	TILABONI UG MINE	2/2019	3/2027 (-) [3/2027]	916.62 (-) [916.62]	0.00 (0.00) [0]
	<u>Health And Family Welfare</u>				
1580	CNCI KOLKATA WEST BENGAL	8/2016	9/2018 (-) [0/0]	244.00 (-) [244.00]	241.39 (0.00) [0]
1581	HOSPITAL AND TEACHING- AIIMS KALYANI	4/2018	/ (-) [2/2020]	651.99 (-) [651.99]	112.82 (0.00) [-]
1582	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	8/2017	3/2019 (-) [3/2020]	355.15 (-) [355.15]	148.84 (0.00) [12]
	<u>Petroleum</u>				
1583	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL	3/2018	9/2022 (-) [6/2021]	3,712.00 (-) [3,696.00]	309.62 (-16.00) [-15]
1584	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY	5/2018	9/2019 (-) [1/2020]	2,934.40 (-) [2,934.40]	1,653.76 (0.00) [4]
1585	DURGAPUR-HALDIA PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	1,740.00 (-) [1,740.00]	275.95 (0.00) [0]
1586	HALDIA BARAUNI PRODUCT PIPELINE	4/2016	12/2020 (-) [12/2020]	1,021.00 (-) [1,021.00]	4.45 (0.00) [0]
1587	HALDIA LPG IMPORT FACILITY	3/2015	10/2018 (12/2019) [12/2019]	694.00 (1,097.54) [1,097.54]	700.96 (403.54) [14]
1588	KHARAGPUR LPG BOTTLING PLANT	4/2017	4/2020 (-) [3/2021]	163.02 (-) [163.02]	50.84 (0.00) [11]
	<u>Power</u>				
1589	DURGAPUR PP-III (2X20 MW) - NSPCL	12/2016	11/2018 (-) [3/2020]	529.68 (-) [529.68]	140.10 (0.00) [16]
1590	EASTERN REGION STRENGTHENING SCHEME-XV	4/2016	4/2018 (-) [1/2020]	454.11 (-) [454.11]	291.64 (0.00) [21]
1591	RAMMAM-III HEPP (3X40 MW)	9/2014	9/2019 (2/2022) [2/2022]	1,381.84 (-) [1,592.34]	486.24 (210.50) [29]
	<u>Railways</u>				
1592	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	4/1998	3/2003 (3/2030) [3/2030]	1,027.40 (-) [2,373.00]	485.04 (1,345.60) [324]
1593	BARDHAMAN-KATWA (GC)	4/2007	12/2010	1,106.62	839.63

			(12/2017) [3/2025]	(-) [1,091.59]	(-15.03) [171]
1594	BAZAR SAU -AZIMGANJ JN. DOUBLING	4/2012	/	255.64	166.12
			(-) [9/2021]	(-) [272.20]	(16.56) [-]
1595	BOWAICHANDI-ARAMBAGH	4/2010	/	267.37	40.99
			(3/2025) [3/2025]	(-) [620.00]	(352.63) [-]
1596	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR	4/2009	/	573.78	0.03
			(-) [3/2025]	(-) [268.52]	(-305.26) [-]
1597	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	3/2013	3/2016	4,874.58	5,892.72
			(-) [6/2021]	(-) [8,574.97]	(3,700.39) [63]
1598	HOWRAH-AMTA-CHAMPADANGA NL (SER)	4/1974	3/2007	393.46	182.49
			(3/2007) [0/0]	(154.30) [1,026.00]	(632.54) [0]
1599	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	4/2010	/	221.42	38.18
			(3/2022) [3/2022]	(-) [380.00]	(158.58) [-]
1600	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	4/1983	3/2019	297.32	274.97
			(-) [3/2020]	(-) [614.00]	(316.68) [12]
1601	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN	2/1999	4/2010	380.60	1,087.60
			(-) [0/0]	(-) [1,871.00]	(1,490.40) [0]
1602	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM)	4/2016	12/2021	602.27	257.73
			(-) [3/2020]	(-) [612.00]	(9.73) [-21]
1603	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	4/2010	3/2014	2,298.42	40.13
			(-) [12/2025]	(-) [2,733.86]	(435.44) [141]
1604	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	4/2010	3/2016	2,913.51	849.88
			(-) [3/2025]	(-) [2,913.50]	(-0.01) [108]
1605	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP)	4/2010	3/2016	2,397.72	197.20
			(-) [0/0]	(-) [2,397.72]	(0.00) [0]
1606	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	4/2010	3/2016	3,951.98	2,237.39
			(-) [3/2025]	(-) [4,259.48]	(307.50) [108]
1607	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	4/2000	3/2019	1,188.91	868.58
			(12/2009) [3/2025]	(-) [1,619.48]	(430.57) [72]
1608	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	3/2000	12/2006	1,049.69	3,837.57
			(-) [0/0]	(-) [3,404.92]	(2,355.23) [0]
	<u>Road Transport And Highways</u>				
1609	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	12/2015	6/2018	1,083.00	26.64
			(-) [12/2019]	(-) [1,083.00]	(0.00) [18]
1610	4-LANING OF BRAHAMPORE-FARAKA	2/2011	8/2013	998.79	1,775.04
			(-) [6/2020]	(-) [998.79]	(0.00) [82]
1611	4-LANING OF FARAKA-RAIGANJ	2/2011	8/2013	1,078.84	2,173.80
			(-) [12/2019]	(-) [1,078.84]	(0.00) [76]
1612	6-LANING OF DHANKUNI-KHARAGPUR SECTION	4/2012	9/2014	1,396.18	2,894.94
			(-) [12/2019]	(-) [1,396.18]	(0.00) [63]
1613	CONSTRUCTION OF ISLAMPUR BY PASS	10/2015	/	361.15	144.71

			(-) [1/2020]	(-) [361.15]	(0.00) [-]
1614	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITTA AND PANITNAKI I	3/2017	6/2018 (-) [0/0]	158.65 (-) [158.65]	33.64 (0.00) [0]
1615	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H	3/2016	11/2018 (11/2019) [11/2019]	271.17 (291.20) [291.20]	80.26 (20.03) [12]
1616	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND	3/2016	8/2019 (-) [8/2021]	160.27 (213.97) [213.97]	20.11 (53.70) [24]
1617	CONSTRUCTION OF ROB –FLYOVER AT RANICHAK, HALDIA	3/2016	11/2018 (-) [12/2019]	229.37 (-) [229.37]	78.31 (0.00) [13]
1618	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N	6/2016	8/2019 (-) [8/2021]	236.78 (263.26) [263.26]	59.92 (26.48) [24]
1619	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO	3/2018	10/2020 (-) [10/2020]	254.30 (254.30) [254.30]	52.85 (0.00) [0]
1620	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA	9/2016	8/2018 (-) [9/2019]	767.03 (767.03) [767.03]	555.72 (0.00) [13]
1621	KRISHNANAGAR-BERHAMPUR	2/2012	7/2014 (-) [6/2020]	702.16 (-) [702.16]	733.33 (0.00) [71]
1622	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O	8/2014	11/2017 (5/2019) [5/2019]	600.87 (720.97) [720.97]	644.60 (120.10) [0]
1623	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O	8/2014	11/2017 (6/2019) [6/2019]	823.20 (937.76) [937.76]	737.80 (114.56) [0]
1624	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA)	3/2018	/ (-) [0/0]	1,261.98 (-) [1,261.98]	0.00 (0.00) [0]
1625	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7	4/2014	8/2017 (7/2019) [7/2019]	279.70 (398.52) [398.52]	315.08 (118.82) [0]
1626	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN	1/2017	9/2019 (-) [0/0]	396.86 (396.86) [396.86]	179.65 (0.00) [0]
1627	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL	1/1991	3/2018 (-) [0/0]	322.00 (-) [322.00]	56.41 (0.00) [0]
1628	SIX-LANING OF BARWA ADDA-PANAGARH	4/2014	/ (-) [0/0]	1,665.00 (-) [1,665.00]	3,059.39 (0.00) [0]
1629	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10	3/2017	11/2019 (-) [11/2019]	202.69 (202.69) [202.69]	93.93 (0.00) [0]
1630	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4	2/2018	11/2020 (-) [11/2020]	218.70 (218.70) [218.70]	37.75 (0.00) [0]
1631	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19.	2/2018	9/2020 (-) [9/2020]	426.18 (426.18) [426.18]	219.94 (0.00) [0]
	<u>Steel</u>				
1632	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E	12/2018	9/2020 (-) [9/2020]	263.36 (-) [263.36]	11.32 (0.00) [0]
	<u>Urban Development</u>				

1633	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	2/2014	8/2016 (-) [10/2019]	156.57 (-) [156.57]	156.13 (0.00) [38]
1634	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG	8/2012	3/2016 (-) [0/0]	185.37 (-) [185.37]	178.30 (0.00) [0]
1635	NSG AT KOLKATA	10/2014	4/2018 (-) [0/0]	162.88 (-) [162.88]	138.89 (0.00) [0]
	Total			19,47,462.67 (5,14,090.22) [23,41,784.84]	9,96,613.94 (3,94,322.17)

North-East Project Detail's

Annexure-XX

Details of Central Sector Projects Costing Rs.150 crore and above (as on					30.09.2019)
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	<u>ARUNACHAL PRADESH</u>				
	<u>Power</u>				
1	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009 (10/2019) [10/2019]	2,496.90 (7,927.34) [7,927.34]	7,579.17 (5,430.44) [118]
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (-) [0/0]	6,285.33 (-) [19,496.34]	10,989.45 (13,211.01) [0]
	<u>Road Transport And Highways</u>				
3	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN	3/2015	/ (-) [0/0]	172.75 (-) [172.75]	112.43 (0.00) [0]
4	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	3/2015	6/2018 (-) [3/2020]	394.00 (-) [394.00]	272.92 (0.00) [21]
5	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59	3/2015	5/2018 (-) [8/2019]	194.11 (-) [194.11]	178.14 (0.00) [0]
6	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS	10/2015	1/2019 (-) [0/0]	179.82 (-) [179.82]	197.77 (0.00) [0]
7	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX	10/2015	/ (1/2016) [1/2019]	210.50 (210.50) [210.50]	117.06 (0.00) [0]
8	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450 TO KM 605.600(EXISTING CHAINAGE FROM KM.583.450	1/2016	11/2016 (-) [0/0]	183.65 (-) [183.65]	98.02 (0.00) [0]
9	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST	11/2016	/ (-) [0/0]	243.89 (-) [243.89]	30.04 (0.00) [0]
10	BORDUMSA NAMCHIK (BURIDEHING - JAIRAMPUR) ROAD ON NH-52B (NEW NH-215) FROM KM. 0.15 (STARTING CHAIN	7/2015	/ (-) [0/0]	189.91 (-) [189.91]	154.43 (0.00) [0]
11	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 37.500 TO KM	5/2016	/ (-) [0/0]	259.52 (-) [259.52]	155.94 (0.00) [0]
12	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120.	12/2016	/ (-) [0/0]	200.44 (-) [200.44]	20.03 (0.00) [0]
13	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50	9/2016	/ (-) [0/0]	568.92 (-) [568.92]	131.32 (0.00) [0]
14	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5	12/2016	/ (-) [0/0]	188.78 (-) [188.78]	38.37 (0.00) [0]

15	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	12/2016	1/2017 (-) [1/2020]	138.93 (155.00) [155.00]	72.97 (16.07) [36]
16	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37	4/2016	/	245.79	98.37
			(-) [9/2020]	(-) [245.79]	(0.00) [-]
17	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM.	4/2016	10/2016 (-) [10/2019]	198.00 (-) [198.00]	155.94 (0.00) [36]
18	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH	7/2015	10/2018 (9/2015) [9/2018]	197.16 (197.16) [197.16]	66.17 (0.00) [0]
19	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF	3/2017	/	1,718.59	158.90
			(-) [0/0]	(-) [1,718.59]	(0.00) [0]
20	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	1/2017	3/2017 (-) [3/2022]	1,253.10 (-) [1,253.10]	158.90 (0.00) [60]
21	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	2/2017	4/2017 (2/2018) [2/2021]	167.28 (167.28) [167.28]	18.94 (0.00) [46]
22	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS	2/2017	4/2017 (2/2018) [2/2021]	216.71 (216.71) [216.71]	16.40 (0.00) [46]
23	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K	3/2018	/	392.60	0.00
			(-) [0/0]	(-) [392.60]	(0.00) [0]
24	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH	11/2015	/	434.06	131.32
			(-) [12/2020]	(-) [434.06]	(0.00) [-]
25	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017 (3/2018) [3/2021]	284.09 (284.09) [284.09]	76.20 (0.00) [47]
26	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017 (-) [0/0]	195.23 (-) [195.23]	37.30 (0.00) [0]
27	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	2/2017	4/2017 (-) [0/0]	203.36 (-) [203.36]	49.12 (0.00) [0]
28	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	194.66 (-) [194.66]	75.04 (0.00) [0]
29	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	198.22 (-) [198.22]	24.14 (0.00) [0]
30	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	3/2012	5/2012 (6/2018) [0/0]	207.03 (389.45) [389.45]	275.19 (182.42) [0]
31	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	2/2017	4/2017 (2/2018) [2/2021]	180.57 (180.57) [180.57]	13.73 (0.00) [46]
32	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS	2/2017	4/2017 (2/2018) [2/2021]	168.32 (168.32) [168.32]	33.51 (0.00) [46]
33	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	12/2011	2/2012 (-) [0/0]	156.63 (276.00) [276.00]	147.65 (119.37) [0]
34	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P	11/2010	3/2011 (-) [0/0]	305.49 (-) [305.49]	131.08 (0.00) [0]
35	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON	1/2017	/	256.66	24.14

	EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI		(-) [0/0]	(-) [256.66]	(0.00) [0]
36	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0	2/2017	/ (4/2019) [4/2022]	175.06 (175.06) [175.06]	12.06 (0.00) [-]
37	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1	2/2017	/ (4/2019) [4/2022]	176.12 (176.12) [176.12]	11.82 (0.00) [-]
38	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 104.850 TO KM 122.600 (D	2/2017	/ (2/2018) [2/2021]	199.02 (199.02) [199.02]	9.81 (0.00) [-]
39	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) ON EPC BASIS FROM EXISTING KM 122.600 TO KM 138.000 (D	2/2017	/ (2/2018) [2/2021]	184.88 (184.88) [184.88]	6.19 (0.00) [-]
40	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU	9/2011	/ (-) [0/0]	1,979.00 (-) [1,979.00]	59.40 (0.00) [0]
	<u>ASSAM</u>				
	<u>Civil Aviation</u>				
41	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	3/2021 (-) [3/2021]	859.86 (-) [860.00]	232.44 (0.14) [0]
	<u>Health And Family Welfare</u>				
42	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021 (-) [10/2021]	875.00 (-) [875.00]	39.27 (0.00) [5]
43	LGBRIMH-TEZPUR, ASSAM	7/2012	12/2014 (-) [0/0]	175.57 (-) [175.57]	113.50 (0.00) [0]
	<u>Petroleum</u>				
44	ASSAM RENEWAL PROJECT FOR GROUP A	3/2009	3/2013 (12/2019) [12/2019]	2,465.15 (-) [2,378.86]	2,147.00 (-86.29) [81]
45	BS VI PROJECT AT GUWAHATI REFINERY	8/2018	2/2020 (-) [2/2020]	557.00 (-) [557.00]	217.83 (0.00) [0]
46	BS-VI PROJECT AT BONGAIGAON REFINERY	5/2018	9/2019 (-) [2/2020]	1,222.00 (-) [1,222.00]	563.53 (0.00) [5]
47	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN	6/2016	8/2020 (-) [8/2020]	224.75 (-) [224.75]	4.37 (0.00) [0]
48	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	7/2011	1/2019 (-) [9/2019]	350.00 (-) [350.00]	2.06 (0.00) [8]
49	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	6/2010	1/2014 (-) [11/2019]	202.94 (345.92) [345.92]	146.58 (142.98) [70]
50	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	6/2016	8/2019 (-) [9/2019]	423.00 (-) [423.00]	263.70 (0.00) [1]
51	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (-) [6/2020]	543.91 (-) [682.90]	8.97 (138.99) [4]
52	INDMAX PROJECT AT BONGAIGAON REFINERY	2/2016	11/2019 (-) [11/2019]	2,582.00 (-) [2,582.00]	1,557.14 (0.00) [0]
53	PIPELINE NETWORK PROJECT GELEKI, ASSAM	7/2016	5/2020 (-) [5/2020]	249.85 (265.49) [265.49]	157.81 (15.64) [0]
54	UPGRADATION OF CRUDE OIL PUMP STATIONS OF	9/2012	3/2015	871.35	565.63

	NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE		(-) [0/0]	(-) [1,200.00]	(328.65) [0]
	<u>Railways</u>				
55	AMBARI FALAKATA TO NEW MAYNAGURI	4/2011	3/2019 (-) [3/2020]	314.00 (728.00) [728.00]	704.09 (414.00) [12]
56	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-) [3/2020]	2,232.32 (-) [2,182.00]	654.38 (-50.32) [-24]
57	DIGARU-HOJAI (102 KM)	4/2015	3/2021 (-) [3/2021]	870.96 (-) [2,136.01]	502.44 (1,265.05) [0]
58	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [3/2020]	385.20 (1,532.00) [1,532.00]	629.19 (1,146.80) [12]
	<u>Road Transport And Highways</u>				
59	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (-) [0/0]	268.08 (-) [268.08]	201.56 (0.00) [0]
60	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	11/2010	2/2011 (-) [0/0]	470.20 (-) [630.36]	344.32 (160.16) [0]
61	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS	12/2015	12/2018 (-) [0/0]	225.02 (-) [159.20]	26.00 (-65.82) [0]
62	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	12/2015	6/2018 (-) [0/0]	223.30 (-) [223.30]	78.89 (0.00) [0]
63	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-) [0/0]	520.01 (-) [520.01]	57.36 (0.00) [0]
64	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [0/0]	588.95 (-) [588.95]	366.26 (0.00) [0]
65	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [0/0]	289.99 (-) [289.99]	20.97 (0.00) [0]
66	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (12/2021) [12/2021]	252.00 (-) [252.00]	4.74 (0.00) [71]
67	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	6/2018 (12/2020) [12/2021]	437.39 (-) [437.39]	9.30 (0.00) [42]
68	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	1/2016 (2/2019) [4/2021]	294.17 (-) [294.17]	63.00 (0.00) [63]
69	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	4/2010 (-) [7/2019]	217.61 (-) [360.84]	451.15 (143.23) [0]
70	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM	11/2010	2/2014 (-) [12/2019]	197.37 (-) [197.37]	88.86 (0.00) [70]
71	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	5/2008 (-) [6/2019]	160.00 (-) [167.98]	223.81 (7.98) [0]
72	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52	6/2016	1/2019 (-) [0/0]	829.00 (-) [829.00]	343.57 (0.00) [0]
73	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [0/0]	168.39 (-) [168.39]	78.89 (0.00) [0]

74	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE	10/2017	/ (-) [6/2020]	818.00 (-) [818.00]	60.08 (0.00) [-]
75	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5	6/2015	6/2018 (1/2021) [12/2021]	463.49 (-) [463.49]	22.32 (0.00) [42]
76	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	3/2015	1/2016 (-) [0/0]	829.00 (-) [829.00]	343.57 (0.00) [0]
77	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (5/2020) [12/2020]	454.89 (-) [454.89]	123.20 (0.00) [31]
78	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	2/2009 (7/2019) [7/2019]	280.00 (456.92) [525.00]	488.37 (245.00) [0]
79	HARANGAJO TO MAIBANG, NH-54	12/2003	7/2009 (10/2018) [10/2018]	196.00 (655.17) [655.17]	655.17 (459.17) [0]
80	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008 (1/2011) [8/2013]	155.04 (255.23) [255.23]	251.39 (100.19) [0]
81	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	4/2009 (3/2011) [8/2019]	199.81 (340.14) [340.14]	319.96 (140.33) [0]
82	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008 (7/2011) [1/2014]	167.64 (408.77) [408.77]	395.78 (241.13) [0]
83	NALBARI T BIJNI (AS-7)	12/2003	4/2008 (-) [3/2020]	208.00 (-) [230.00]	337.76 (22.00) [143]
84	NALBARI TO BIJNI (AS-6)	12/2003	6/2008 (-) [10/2019]	225.00 (-) [225.00]	328.47 (0.00) [136]
85	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST	3/2017	/ (-) [0/0]	1,049.51 (-) [1,049.51]	86.70 (0.00) [0]
86	SONAPUR TO GUWAHTI (AS-3)	12/2003	3/2008 (-) [8/2020]	245.00 (-) [174.34]	224.28 (-70.66) [149]
87	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ	11/2014	2/2018 (-) [0/0]	218.31 (307.47) [307.47]	256.26 (89.16) [0]
88	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN	9/2018	9/2021 (-) [9/2021]	160.00 (-) [160.00]	0.50 (0.00) [0]
<u>MANIPUR</u>					
<u>Power</u>					
89	LOKTAK D/S HEP(NHPC)	12/1999	6/2006 (-) [0/0]	578.62 (-) [578.62]	0.00 (0.00) [0]
<u>Railways</u>					
90	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (-) [3/2020]	4,454.17 (13,809.00) [12,524.00]	9,123.93 (8,069.83) [108]
<u>Road Transport And Highways</u>					
91	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260.	10/2016	11/2020 (-) [11/2020]	235.31 (-) [235.31]	91.38 (0.00) [0]
92	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	8/2017	10/2018 (-) [10/2021]	517.57 (-) [457.77]	137.04 (-59.80) [36]

	<u>Urban Development</u>				
93	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	2/2014	3/2015 (-) [10/2020]	216.69 (-) [216.69]	52.00 (0.00) [67]
	<u>MEGHALAYA</u>				
	<u>Health And Family Welfare</u>				
94	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (-) [9/2019]	363.99 (-) [363.99]	166.19 (0.00) [16]
	<u>Railways</u>				
95	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [3/2021]	906.46 (-) [6,000.00]	261.76 (5,093.54) [0]
	<u>Road Transport And Highways</u>				
96	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	3/2019	5/2019 (-) [0/0]	306.28 (-) [306.28]	42.66 (0.00) [0]
97	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	12/2015	5/2018 (3/2018) [10/2019]	479.20 (-) [479.20]	711.38 (0.00) [17]
98	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	/ (-) [9/2021]	553.51 (-) [553.51]	27.90 (0.00) [-]
	<u>Urban Development</u>				
99	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCP	4/2014	9/2017 (-) [0/0]	151.33 (-) [151.33]	7.15 (0.00) [0]
	<u>MIZORAM</u>				
	<u>Railways</u>				
100	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (3/2022) [3/2022]	2,393.47 (4,968.00) [5,021.45]	3,075.08 (2,627.98) [96]
	<u>Road Transport And Highways</u>				
101	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (-) [6/2020]	195.04 (-) [377.99]	305.38 (182.95) [116]
102	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	9/2014 (-) [12/2019]	186.96 (-) [305.61]	275.06 (118.65) [63]
103	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (-) [12/2019]	193.69 (-) [327.92]	254.24 (134.23) [110]
104	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	519.09 (-) [519.09]	0.00 (0.00) [0]
105	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	537.82 (-) [537.82]	0.00 (0.00) [0]
106	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	404.29 (-) [404.29]	0.00 (0.00) [0]
107	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	428.11 (-) [428.11]	0.00 (0.00) [0]
108	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	518.53 (-) [518.53]	0.00 (0.00) [0]
109	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	473.18 (-) [473.18]	0.00 (0.00) [0]
110	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED	4/2017	9/2019	640.07	0.00

	SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO		(-) [9/2019]	(-) [640.07]	(0.00) [0]
111	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	642.96 (-) [642.96]	0.00 (0.00) [0]
112	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (-) [12/2019]	624.41 (-) [992.67]	853.82 (368.26) [105]
	<u>NAGALAND</u>				
	<u>Railways</u>				
113	DIMAPUR-TIZIT NL	4/2013	3/2020 (-) [3/2020]	4,274.00 (-) [4,274.00]	0.00 (0.00) [0]
114	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015 (-) [10/2021]	2,326.52 (-) [4,600.00]	781.71 (2,273.48) [79]
	<u>Road Transport And Highways</u>				
115	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018 (5/2019) [0/0]	239.30 (-) [239.30]	0.00 (0.00) [0]
116	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	3/2018	9/2018 (-) [0/0]	285.68 (-) [285.68]	0.00 (0.00) [0]
117	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	3/2018	9/2018 (11/2018) [0/0]	282.98 (-) [282.98]	12.76 (0.00) [0]
118	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018 (-) [0/0]	387.00 (-) [387.00]	135.12 (0.00) [0]
119	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	9/2018 (-) [0/0]	500.09 (-) [500.09]	0.00 (0.00) [0]
120	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN	3/2017	11/2020 (-) [11/2020]	217.35 (-) [217.35]	35.10 (0.00) [0]
121	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683	2/2017	4/2017 (-) [0/0]	507.68 (-) [507.68]	129.13 (0.00) [0]
122	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (7/2019) [0/0]	339.57 (233.35) [339.57]	0.00 (0.00) [0]
123	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	3/2018	9/2018 (-) [0/0]	315.03 (-) [315.03]	4.38 (0.00) [0]
124	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	9/2018 (-) [0/0]	240.64 (-) [240.64]	2.11 (0.00) [0]
125	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [0/0]	215.12 (-) [215.12]	10.07 (0.00) [0]
126	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	9/2018 (-) [0/0]	215.79 (-) [215.79]	0.00 (0.00) [0]
127	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [0/0]	272.89 (-) [272.89]	0.00 (0.00) [0]
128	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	3/2018	9/2018 (-) [0/0]	323.98 (-) [323.98]	0.00 (0.00) [0]
129	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900	3/2018	9/2018 (11/2018)	251.97 (160.10)	16.63 (0.00)

	TO KM40.0		[0/0]	[251.97]	[0]
130	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (11/2018) [0/0]	237.72 (136.73) [237.72]	21.71 (0.00) [0]
131	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	8/2016 (-) [8/2019]	373.07 (387.00) [373.07]	209.22 (0.00) [0]
132	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2016 (-) [6/2020]	396.52 (339.55) [396.52]	234.03 (0.00) [46]
133	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	3/2016	8/2016 (-) [8/2019]	429.52 (340.00) [429.52]	166.55 (0.00) [0]
134	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M	11/2016	9/2019 (-) [9/2019]	336.25 (369.96) [336.25]	62.64 (0.00) [0]
135	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (-) [12/2020]	167.62 (-) [167.62]	42.15 (0.00) [0]
136	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (-) [12/2020]	172.63 (-) [172.63]	45.02 (0.00) [0]
137	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA	12/2010	2/2011 (-) [0/0]	1,296.00 (-) [1,296.00]	0.00 (0.00) [0]
138	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH-	3/2019	12/2022 (-) [12/2022]	237.51 (-) [237.51]	0.00 (0.00) [0]
	<u>SIKKIM</u>				
	<u>Railways</u>				
139	SEVOK RANGPO, NEFR	4/2008	12/2015 (-) [0/0]	1,339.48 (-) [4,084.69]	285.46 (2,745.21) [0]
	<u>Road Transport And Highways</u>				
140	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	1/2013	2/2013 (9/2017) [12/2019]	182.28 (269.14) [269.14]	185.49 (86.86) [82]
141	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	4/2013	8/2013 (-) [12/2019]	151.59 (240.58) [151.59]	196.76 (0.00) [76]
142	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM.	4/2013	8/2013 (-) [0/0]	166.27 (203.26) [166.27]	141.31 (0.00) [0]
143	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	3/2017	/ (-) [0/0]	375.80 (-) [375.80]	77.39 (0.00) [0]
144	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	11/2017	11/2017 (-) [0/0]	290.05 (-) [290.05]	33.95 (0.00) [0]
145	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA	4/2017	11/2017 (-) [0/0]	318.42 (-) [318.42]	97.85 (0.00) [0]
146	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	3/2018	6/2018 (-) [0/0]	264.84 (-) [264.84]	0.00 (0.00) [0]
147	RHENOK-RORATHANG-PAKYONG ON NH 717A	4/2017	10/2017 (-) [0/0]	388.00 (-) [447.37]	103.82 (59.37) [0]
	<u>TRIPURA</u>				
	<u>Civil Aviation</u>				
148	CONSTRUCTION OF NEW INTEGRATED TERMINAL	9/2015	6/2019	338.93	213.50

	BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT		(-) [12/2019]	(-) [339.00]	(0.07) [6]
	<u>Railways</u>				
149	AGARTALA-AKHAURA NL	4/2012	3/2020 (-) [12/2021]	569.63 (-) [650.00]	45.24 (80.37) [21]
	<u>Road Transport And Highways</u>				
150	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S	10/2014	3/2018 (12/2019) [12/2019]	369.00 (-) [369.00]	308.97 (0.00) [21]
151	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C	10/2016	8/2020 (-) [8/2020]	171.90 (-) [171.90]	11.75 (0.00) [0]
	<u>Urban Development</u>				
152	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	3/2007	12/2015 (-) [0/0]	149.73 (173.00) [175.94]	178.65 (26.21) [0]
153	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016 (-) [0/0]	202.61 (227.00) [227.00]	199.95 (24.39) [0]
154	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	12/2016 (-) [0/0]	175.49 (206.71) [206.71]	141.28 (31.22) [0]
	Total			84,828.31 (38,265.99) [1,30,437.95]	56,216.47 (45,609.64)
