

**299th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹.150 Crores and above)
September, 2010**



HPCL – Mumbai Refinery



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Contents

Executive Summary	1 -5
Month wise list of completed projects Costing Rs. 150 Crore and Above During 2010-11	6-8
List of Delete Projects	9-9
Summary of Projects	10-23
Sector wise Trend and Graphicalf Analysis	24-32
Sector wise analysis of projects	33-62
Graph	63-72
List of All Ongoing Projects	73-73
List of Abbreviations	74-76

EXECUTIVE SUMMARY

The 299th Flash Report for September' 2010, that contains information on the status of 606 projects in the Central Sector, each costing Rs. 150 Crores and above. Since April' 2010, Flash report is prepared for the central sector projects costing Rs 150 Crores and above. During September' 2010, 47 projects reported completion. Five projects have been added during the month under reference. During September' 2010, total five projects in Power sector have shown considerable improvement over the completion schedule reported earlier.

The online submission of the implementation Status Report of the ongoing projects has significantly improved as in September, 2010 nearly 90% projects reported online.as . Out of 553 ongoing projects on the monitor of this Ministry, 496 projects were updated either by the concerned project agencies online or the data has been entered locally by the staff of this Ministry. The information regarding 5 projects only were not updated/received by this Ministry. Sector-wise number of ongoing projects along with status of online reporting is given below:

S. No.	Sector	Projects on monitor	Reported Online	Additional delays
1.	ROAD TRANSPORT & HIGHWAYS	116	116	52
2.	RAILWAYS	129	91	5
3.	POWER	85	80	23
4.	PETROLEUM	70	66	14
5.	COAL	44	44	3
6.	TELECOMMUNICATION	47	47	17
7.	STEEL	16	16	5
8.	SHIPPING & PORTS	22	20	2
9.	CIVIL AVIATION	9	6	-
10.	FERTILISERS	6	4	4
11.	ATOMIC ENERGY	4	3	1
12.	URBAN DEVELOPMENT	2	1	1
13.	MINES	1	1	-
14.	HEALTH & FW	1	1	-
15.	WATER RESOURCES	1	-	-
Total		553	496	127

2. One hundred and twenty seven (127) projects have reported additional delays compared to the completion dates in the previous month. Five projects in Power sector have shown considerable improvement over the completion schedule reported earlier.

- 2.1 The additional delays are in the range of 1 to 24 months in respect of projects relating to Coal, Steel, Petroleum, Power, Railways, Road Transport and Highways, Shipping & Ports, Telecommunications and Urban Development Sectors.
2. Out of 553 projects, 16 projects are ahead of schedule, 108 are on schedule and 292 projects are delayed. Of the balance, 83 projects do not have fixed dates of commissioning i.e. either the year of commissioning or the tentative gestation period of the projects have been reported. A large number of projects (54) were sanctioned without any commissioning schedule/date.
 4. The total cost of implementation of 553 projects when sanctioned, was of the order of Rs. 569479.67 Crores but this was subsequently revised to Rs. 691003.22 Crores implying a cost overrun of 21.30%. The expenditure incurred on these projects till September, 2010 is Rs. 285920.13 Crores which is 41% of the revised cost of the projects.
 5. To present a concise picture of the status of on-going projects costing ₹ 150 Crores and above, a pictorial presentation is given in the report. Out of 553 projects, presently on the monitor at the end of September 2010, 108 projects were on schedule (19%), excluding 83 projects without date of commissioning and those have not reported during the month, 292 projects were delayed (52%). During the month, 127 projects have reported additional delays in the range of 2-24 months. The analysis of pictorial presentation shows that since June, 2010 there is a continuous decrease in projects reporting delays. The overall cost overrun is on the rise continuously since June 2010. The overall cost overrun has increases from 17% in June to 21.3% in September 2010 due to substantial increase in the completion costs of Expansion of Bokaro Steel Plant and Bhilai Steel Plant by Rs 15089 Crores. It may be seen that out of 292 delayed projects, at the end of September, 2010, 80 projects had overall delay in the range of 1 to 12 months, 80 projects had delay in the range of 13 to 24 months, 103 projects had delay in the range of 25 to 60 months and 29 projects had time overrun of 61 months and above.
 7. In the **Coal sector**, 3 projects have reported additional delays in the range of 1-24 months. Bhubaneswari OCP has reported additional delay of 12 months due to delay in environment clearances. Gevera Expansion OCP (SECL) has reported additional delay of 24 months due to delay in finalization of tender process. Block-B OCP, NCL has reported additional delay of 24 months due to delay in acquisition of land, forest clearance and delay in rehabilitation.
 8. In the **Steel Sector**, 5 projects have reported additional delay of 1-3 months. Installation of 700 TPD Oxygen Plant, Rourkela and Simultaneous Blowing of BOF Converter of SMS-II & Expansion of Salem Steel Plant have reported additional delay of 2 months each due to delay in supply of equipments. Rebuilding of Coke Oven Battery No. 1 & 2 and Rebuilding of Coke Oven Battery No - 6 have reported additional delay of 3 months each due to delay in supply of fireclay bricks.
 9. In the **Petroleum Sector**, 14 projects have reported additional delays in the range of 1-6 months, whereas one project has shown considerable improvement over the completion schedule reported earlier. Installation of FCCU at Mumbai refinery has reported improvement of 1 months due to availability of raw material. MSQ Improvement project has reported additional delay of 1 month due to delay in installation and drilling work by the contractor. Additional Gas processing units at (ONGC) Uran, Mumbai has reported

additional delay of 2 months due to delay in tender process. MSQ Upgradation Project at Guwahati Refinery and MSQ Upgradation Project at Digboi Refinery have reported additional delay of 1 month and 2 months due to poor response to consultancy bids, frequent bands and insufficient transportation of material/equipment. MSQ Upgradation Project at Barauni Refinery has reported additional delay of 1 month due to backing out of reputed PSU consultants in last moment, slow progress by M/S BHEL in power plant jobs and delay by BHPV in supply of compressor package by 11 month. Capacity Expansion cum Modernisation Phase-II project has reported additional delay of 1 month due to slow progress by the contractor. BNPL Spurline (Uttaranchal & Punjab) project has reported additional delay of 1 month due to slow progress because of problems in North East. Diesel Hydro Treatment Project, BRPL Dhauligaon project has reported additional delay of 2 months due to local constraints like scares technical resources in this region. Vijaypur Dadri-Bawana Pipeline Project has reported additional delay of 2 months due to resistance from farmers demanding high compensation. Sultanpur Neemrana Pipe Line Project has reported additional delay of 2 months, however, no specific reason has been given by the project authority. Construction of New Terminal at Ennore, Chennai has reported additional delay of 2 months due to slow progress. Compressor Stations (Vijaypur and Jhabua) Phase-1 project has reported additional delay of 6 months due to delay in supply of equipments & bad weather.

10. In the **Power Sector**, 18 projects have reported additional delays in the range of 1-18 months, whereas 5 projects have reported considerable improvement over the completion schedule reported earlier. Teesta Low Dam Stage- IV has reported additional delay of 12 months due to delay in forest clearance and delay in decision regarding participation of Chinese firm and strike by GJMM. Tehri Pumped Storage Plant has reported additional delay of 3 months due to delay in award of contract. Transmission System for Startup Power to DVC & Maithon RB Generation project (PGCIL) has reported additional delay of 3 months due to delay in forest clearance. Rihand STPP Stage-III have reported additional delay of one month each, however, no specific reasons have been provided by the project authorities for such additional delays. Transmission System Associated with Barh Generation Project, Power Grid Corporation of India Ltd has reported additional delay of 3 months to match the requirement of linked Generation project. BARH STPP, 3x660 MW has reported additional delay of 2 months due to continued delay in supply of material by M/s Power Machine, Russia. Kunadankulam-APP Transmission system (PGCIL) has reported additional delay of 6 months due to stiff resistance from locals and pending court cases. Chamara, Hydro Electric Project Stage III (NHPC) has reported additional delay of 8 months due to violence among contractor's laborers and court stay on crushing Plant leading to huge shortage of aggregate for concrete work. Nimoo Bazo Hydro Electric Project has reported additional delay of 7 months due to highly inclement weather condition, delay in award of E&M works due to poor participation, delay in HM works due to abnormal high price bid and retendering thereof. Western Region Transmission Strengthening Scheme has reported additional delay of 5 months to match with the linked generation project. KORBA STPP Stage-III has reported additional delay of 1 month, due to slow progress of work and delay in supply of equipments. Western Region Strengthening Scheme VI have reported additional delay of 1 month due to severe ROW problems. The reasons of delay in respect of other projects (Table VIII may be referred) have not been reported by the project authorities.

11. In the **Road Transport and Highways Sector**, 52 projects (Table VIII may be referred) have reported additional delay in the range of 1-36 months. General reasons of delay in meeting the completion schedule include delay in land acquisition, utility shifting, Termination of contracts due to poor performance and delay in getting the forest clearance, slow progress of work by the contractor, local constraints, inclement weather conditions and revision of scope of works. However, the project authorities have not mentioned any specific reason for such additional delays.
12. In the **Railway Sector**, 5 projects have shown additional delays in the range of 9-13 months. Jind-Sonepat (NL) has reported additional delay of 9 months, due to revised estimate under finance vetting and delay in land acquisition. Chandigarh-Ludhiana (New BG Line), (NR) has reported additional delay of 12 months, second estimate submitted to Railway Board for sanction. Utratia – Zafrabad (LD) has reported additional delay of 12 months due to delay in tendering process. Mumbai Urban Transport Project Phase-II has reported additional delay of 12 months, delay due to resettlement & rehabilitation of project affected households. Talcher-Bimlagarh (NL) has reported additional delays of 13 months due to delay in land acquisition by State Government and delay in tendering process.
13. In the **Shipping & Ports Sector**, 2 projects namely Deepening of Channel at Paradip Port and Acquisition of 2 Nos. of 105000 DWT LR-II Tankers of Shipping Corporation of India, Maharashtra have shown additional delays in the range of 3-4 months. However, no specific reasons have been given by the project authorities for such additional delays.
14. In the **Telecommunication Sector**, 17 projects (Table VIII may be referred) have shown additional delays of 1 – 4 months. General reasons of delay in meeting the completion schedule include delay in land acquisition, Erection of BITS, Termination of contracts due to poor performance, slow progress of work by the contractor, local constraints, inclement weather conditions and revision of scope of works. However, the project authorities have not mentioned any specific reason for such additional delays.
14. In the **Urban Development Sector**, Delhi MRTS Phase-II Project has reported additional delay of 1 month due to delay in releasing of funds.

Status as on 01.10.2010 in respect of completion of projects costing Rs.150 Crores and above in different sectors during 2010-11 is indicated in the Report.

(Pankaj Jain)

**Additional Secretary to the Government of India
Ministry of Statistics & Programme Implementation**

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Additional Delayed
1	Railways	129	5
2	Road Transport & Highways	116	52
3	Power	85	23
4	Petroleum	70	14
5	Telecommunications	47	17
6	Coal	44	3
7	Shipping & Ports	22	2
8	Steel	16	5
9	Civil Aviation	9	0
10	Fertilisers	6	4
11	Atomic Energy	4	1
12	Urban Development	2	1
13	Mines	1	0
14	Health & Family Welfare	1	0
15	Water Resources	1	0
	Total	553	127

ANNEXURE-I

Month wise List of Completed Project Costing Rs. 150 Crore and above during 2010-2011

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
May,2010				
<u>Petroleum</u>				
1	SHORT TERM LOW COST MUMBAI REFINERY(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000082]	390.00	01/2010	188.43
June,2010				
<u>Steel</u>				
2	REBUILDING OF COKE OVEN BATTERY NO.-4(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000021]	248.94	08/2009	164.48
<u>Petroleum</u>				
3	CLEAN FUELS PROJECT AT VISAKH REFINERY(HPCL)(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [160100281]	1,635.00	05/2006	2,095.36
<u>Telecommunications</u>				
4	EXPANSION OF 750K GSM LINES(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000049]	.00	12/2008	175.77
5	DELHI EXP. OF 1250K LINES OF 2G/3G GSM LINES(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000052]	463.61	12/2009	106.13
July,2010				
<u>Petroleum</u>				
6	BARGE BUMPER-BOAT LANDING-RISER PROTECTOR PROJECT(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000055]	289.60	05/2010	198.16
7	BINA KOTA PIPE LINE PROJECT(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000079]	405.82	12/2009	354.93
September,2010				
<u>Coal</u>				
8	BARSINGSAR MINE 2.10 MTPA LIGNITE (NLC)(NEYVELI LIGNITE CORPORATION) - [060100090]	254.07	06/2009	1,687.78
<u>Steel</u>				
9	REBUILDING OF COKE OVEN BATTERY-10(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000016]	416.50	09/2009	305.14
<u>Petroleum</u>				

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2010-2011**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
10	PANIPAT NAPHTA CRACKER PROJECT(INDIAN OIL CORPORATION LIMITED) - [160100292]	14,439.00	11/2009	12,054.37
11	DADRI- PANIPAT R-LNG SPUR PIPELINE(INDIAN OIL CORPORATION LIMITED) - [N16000018]	250.66	06/2008	350.96
12	LUBE OIL BASE STOCK QUALITY UPGRADATION AT MUMBAI REFINERY(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000026]	638.90	04/2009	796.21
13	INST. OF FCC GASOLINE DESULPHUR UNIT AT MATHURA RE(INDIAN OIL CORPORATION LIMITED) - [N16000034]	348.00	12/2009	186.58
14	MSQ UPGRADATION PROJECT AT PANIPAT REFINERY(INDIAN OIL CORPORATION LIMITED) - [N16000035]	1,131.00	12/2009	750.71
15	CHAINSAR-JHAJJAR PIPE LINE PROJECT(GAS AUTHORITY OF INDIA LIMITED) - [N16000047]	967.77	09/2009	416.90
16	SINGLE POINT MOORING PROJECT AT VISAKHAPATNAM(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000067]	643.46	-	726.45
17	Construction of Tank and Blending Facility at Vadi(INDIAN OIL CORPORATION LIMITED) - [N16000075]	267.00	-	72.99
18	BINA DESPATCH TERMINAL(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000078]	490.71	12/2009	590.52
<u>Railways</u>				
19	HOSPET-GUNTAKAL(LD),SCR(RAIL VIKAS NIGAM LTD.) - [220100195]	105.22	12/1999	283.49
20	NEW JALPAIGURI-NEW BONGAIGAON (GC),NEFR(NORTH EAST FRONTIER RAILWAY) - [220100224]	536.85	03/2003	1,005.50
21	TAHANJAVUR-VILLUPURAM GAUGE CONVERSION (G.C)(SR)(RAIL VIKAS NIGAM LTD.) - [220100244]	223.00	-	586.85
22	AJMER-PHULERA-RINGUS-REWARI (G.C.)(NWR)(RVNL)(RAIL VIKAS NIGAM LTD.) - [N22000033]	352.00	03/2008	616.44
23	ABOHAR- FAZILKA, NR, NL(NEW LINE) - [N22000055]	86.44	03/2009	201.79
<u>Road Transport & Highways</u>				
24	ALLAHABAD BYPASS (KM.158-KM.198) GQ, NH-2(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240100203]	440.93	12/2006	641.40
25	ALLAHABAD BYPASS (KM.198-KM.242.708) GQ, NH-2(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240100204]	534.39	05/2007	716.15
26	FATEHPUR-KHAGA (GQ) KM.38-KM.115 (NH-2)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240101178]	372.40	07/2004	406.05
27	VARANASI-MOHANIA (GQ) KM.317-329 & KM.0-KM.65 (NH-2)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240101181]	467.93	03/2005	453.64
28	GORHAR-BARWA ADDA (GQ) KM.320-KM.398.75 (NH-2)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240101187]	399.75	03/2005	424.96
29	PURNEA-FORBESGANJ (BR-1) PHASE-II, KM.309 TO 268, NH-57(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106227]	276.00	04/2008	360.00
30	PURNEA-FORBESGANJ (BR-2) PHASE-II, KM.268 TO 230, NH-57(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106228]	310.00	04/2008	392.26
31	MADURAI -KANNIAKUMARI SEC. (NS-42/TN) NH-7, KM.120 TO KM.160(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106241]	507.49	03/2008	342.80
32	DHULE-PIMPALGAON, NH-3, KM.380 TOKM. 265(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106257]	556.00	03/2009	568.50

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2010-2011**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
33	SALEM TO KERALA BORDER SEC(TN6), KM.203.96 NH7 TO KM 53 NH47(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106273]	469.80	12/2008	665.80
34	TRICHY BYPASS END TO TOVARAMKURCHI (NH-45B)(NHA)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106285]	261.00	08/2008	286.30
35	TOVARAMKURCHI-MADURAI,NH45B (NHA)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000054]	263.00	08/2008	317.74
36	AP/KARNATKA BORDER-NANDI HILL CROSSING AND DEVANHA(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000060]	402.80	03/2009	453.70
37	PADALUR-TRICHY, NH-45(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000083]	320.00	05/2009	636.10
38	MAHARASHTRA/AP BORDER TO ISLAM NAGAR,(NS-2/BOT/AP-6),NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000093]	360.42	11/2009	478.40
39	ELEVATED HIGHWAY FROM SILK BOARD JUNCTION TO ELECT(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000105]	450.00	07/2008	876.61
40	ISLAM NAGAR TO KADTAL(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000109]	546.83	03/2010	667.80
41	WAINGANGA BRIDGE -CHHATISGARH-MAHARASHTRA(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000120]	424.00	09/2010	298.40
Shipping & Ports				
42	ACQUISITION OF TWO NOS.OF 470000 DWT MR TANKERS(SHIPPING corp. of india) - [N25000013]	411.32	03/2010	406.28
43	DEV. & OPRATION OF AN INTERNATIONAL CONTAINER TRA(PORT TRUST) - [N25000046]	2,118.00	11/2004	.00
Telecommunications				
44	NATIONAL RADIO SPECTRUM MANAGEMENTand MONIT. SY. I(DEPARTMENT OF TELECOMMUNICATION) - [260100051]	279.97	12/2004	136.24
45	GSM EXPANSION PH.IV (B) (BSNL) MAHARASHTRA(BHARAT SANCHAR NIGAM LIMITED) - [260100095]	1,174.75	03/2006	371.41
46	EXP. OF 750K GSM LINES OF 2.5 GSM AND VALIDATION EQU(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000026]	741.77	10/2007	151.37
47	COMMISSIONING OF GSM EQUIPMENT OF 650K LINES (PH-(BHARAT SANCHAR NIGAM LIMITED) - [N26000028]	364.52	-	51.44
48	GSM EQUIPMENT OF 1006280 LINES IN TAMILNADU PH-4.5(BHARAT SANCHAR NIGAM LIMITED) - [N26000042]	409.21	12/2008	470.24
49	EXPANSION OF EXISTING 2G&3G GSM N/W BY 750 KPE NO(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000061]	180.53	12/2009	25.97

ANNEXURE-I

Month wise List of Deleted Project Costing Rs. 150 Crore and above during 2010-2011

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
September, 2010				
<u>Petroleum</u>				
1	CAPACITY EXPANSION AND MODERNISATION OF KOCHI REFINERY (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000082]	2,591.80	09/2009	1,793.00
<u>Road Transport & Highways</u>				
2	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N12000021]	300.00	10/2008	.00


Summary of projects on the Flash Report for the month of Sept, 2010

I. Project Implementation – Current Status:

Number of Projects Cost (Rs. 150 Cr. & above) Previous Month	606
Number of Projects Completed/Dropped/Frozen Cost (Rs. 150 Cr. & above) in Previous Month	0
Number of Projects Completed/Dropped/Frozen Cost (Rs. 150 Cr. & above) in Current month	47
No. of projects with Anticipated less then Rs. 150 Cr in Current Mont	6
No. of Projects Duplicates in Current Month	5
Number of Projects Cost (Rs. 150 Cr. & above) Added in Current month	5
Number of Projects Cost (Rs. 150 Cr. & above) in Current Month	553

II. Brief Analysis


a) **Project Status w.r.t Original Schedule:** Out of 553 projects, 16 projects are ahead of schedule, 108 projects are on schedule and 292 projects are delayed. Of the balance, 83 projects do not have fixed dates of commissioning while 54 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

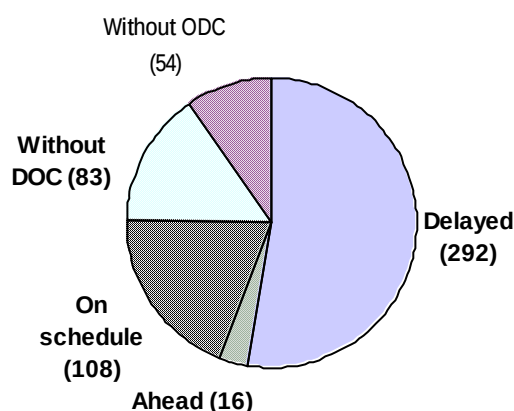

III. Investment Scenario

Figures are in Rs. Crore

The total Original cost of implementation of 553 projects when sanctioned, was of the order of Rs. 569479.67 crore but this was subsequently revised to Rs. 691003.22 crore implying a cost overrun of 21.30%. The expenditure incurred on these projects till Sept, 2010 is Rs. 285920.13 crore, which is 41.38% of the revised cost of the projects.

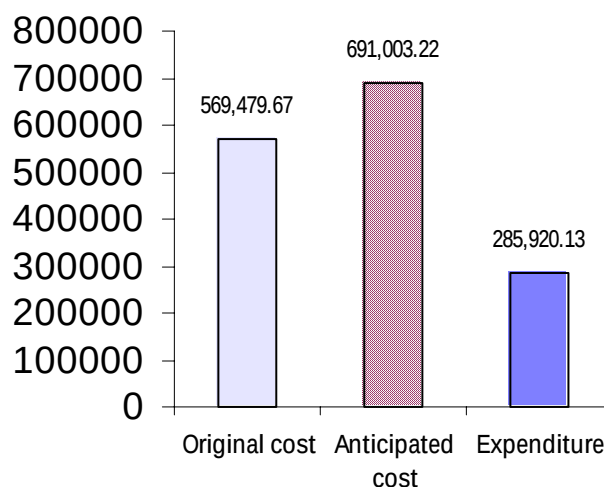

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	606
No of Projects Completed/Dropped/Frozen in Previous Month	0
No of Projects Completed/Dropped/Frozen in Current Month	47
No. of projects with Anticipated less then Rs. 150 Cr in Current Month	6
No. of Projects Duplicates in Current Month	5
No of Projects added in Current Month	5
No of Projects in Current Month	553

II. Project status

With Respect To	Number of Projects						Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total	
Original (Date)	292	16	108	54	83	553	52.80
Latest Approved (Date)	285	15	137	42	77	553	51.54

III. (A) Project cost

(Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	458	474,763.59	522,539.31	201,222.35	38.50	47,775.72	10.10
Latest Approved (RCE)	95	140,114.75	168,463.91	84,697.78	50.30	28,349.16	20.20
Total (RCE)	553	614,878.34	691,003.22	285,920.13	41.38	76124.88	12.38
Original Cost of All Projects							
Original Cost	553	569,479.67	691,003.22	285,920.13	41.40	121,523.55	21.30

III. (B) Delayed Project cost

(Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	292	296,197.93	362,632.14	199,983.77	55.10	66,434.21	22.40
Latest Approved (RCE)	285	300,582.01	346,815.26	195,048.95	56.20	46,233.25	15.40
Total	577	596,779.94	709,447.40	395,032.72	55.68	112667.46	18.88

IV. Additional Delayed Project cost

(Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Latest Approved	127	142,576.13	159,960.82	97,343.55	60.90	17,384.69	12.20
Total	127	142,576.13	159,960.82	97,343.55	60.85	17384.69	12.19

V. List of projects completed/dropped current month

(Cost /Expenditure in Rs. crore)

Project	DOA	Original		Now anticipated		Final
		Cost	DOC	Cost	DOC	Expenditure
<u>Coal</u>						
BARSINGSAR MINE 2.10 MTPA LIGNITE (NLC)	12/2004	254.07	06/2009	1,687.78	09/2010	1,687.78
<u>Petroleum</u>						
PANIPAT NAPHTA CRACKER PROJECT	04/2006	14,439.00	11/2009	15,292.00	N.A.	12,054.37
<u>Railways</u>						
HOSPET-GUNTAKAL(LD),SCR	03/1996	105.22	12/1999	268.00	09/2010	283.49
NEW JALPAIGURI-NEW BONGAIGAON (GC),NEFR	11/1998	536.85	03/2003	1,010.00	09/2010	1,005.50
TAHANJAVUR-VILLUPURAM GAUGE CONVERSION (G.C)(SR)	10/2001	223.00	N.A.	665.00	09/2010	586.85
<u>Road Transport & Highways</u>						
ALLAHABAD BYPASS (KM.158-KM.198) GQ, NH-2	04/2000	440.93	12/2006	440.93	N.A.	641.40
ALLAHABAD BYPASS (KM.198-KM.242.708) GQ, NH-2	04/2000	534.39	05/2007	534.39	N.A.	716.15
FATEHPUR-KHAGA (GQ) KM.38-KM.115 (NH-2)	04/2000	372.40	07/2004	372.40	10/2010	406.05
VARANASI-MOHANIA (GQ) KM.317-329 & KM.0-KM.65 (NH-2)	04/2000	467.93	03/2005	467.93	10/2010	453.64
GORHAR-BARWA ADDA (GQ) KM.320-KM.398.75 (NH-2)	04/2000	399.75	03/2005	399.75	10/2010	424.96
PURNEA-FORBESGANJ (BR-1) PHASE-II, KM.309 TO 268, NH-57	12/2003	276.00	04/2008	276.00	N.A.	360.00
PURNEA-FORBESGANJ (BR-2) PHASE-II, KM.268 TO 230, NH-57	12/2003	310.00	04/2008	310.00	N.A.	392.26
MADURAI -KANNIAKUMARI SEC. (NS-42/TN) NH-7, KM.120 TO KM.160	12/2003	507.49	03/2008	507.49	08/2010	342.80

V. List of projects completed/dropped current month

(Cost /Expenditure in Rs. crore)

Project	DOA	Original		Now anticipated		Final
		Cost	DOC	Cost	DOC	Expenditure
DHULE-PIMPALGAON, NH-3, KM.380 TOKM. 265	03/2005	556.00	03/2009	556.00	N.A.	568.50
SALEM TO KERALA BORDER SEC(TN6), KM.203.96 NH7 TO KM 53 NH47	12/2003	469.80	12/2008	469.80	N.A.	665.80
TRICHY BYPASS END TO TOVARAMKURCHI (NH-45B)(NHAI)	03/2005	261.00	08/2008	261.00	N.A.	286.30
<u>Telecommunications</u>						
GSM EXPANSION PH.IV (B) (BSNL) MAHARASHTRA	07/2005	1,174.75	03/2006	1,174.75	09/2010	371.41
<u>Steel</u>						
AIR SEPARATION PLANT (ASU-4)	03/2008	96.00	06/2010	170.00	N.A.	42.02
<u>Petroleum</u>						
CAPACITY EXPANSION AND MODERNISATION OF KOCHI REFINERY	04/2006	2,591.80	09/2009	3,941.41	09/2010	1,793.00
CHAINSA-JHAJJAR PIPE LINE PROJECT	11/2007	967.77	09/2009	571.64	03/2010	416.90
<u>Railways</u>						
AJMER-PHULERA-RINGUS-REWARI (G.C.)(NWR)(RVNL)	04/2005	352.00	03/2008	718.30	09/2010	616.44
ABOHAR- FAZILKA, NR, NL	09/2001	86.44	03/2009	209.57	09/2010	201.79
<u>Road Transport & Highways</u>						
TOVARAMKURCHI-MADURAI,NH45B (NHAI)	04/2000	263.00	08/2008	263.00	N.A.	317.74
AP/KARNATKA BORDER-NANDI HILL CROSSING AND DEVANHA	12/2003	402.80	03/2009	402.80	N.A.	453.70
PADALUR-TRICHY, NH-45	03/2005	320.00	05/2009	320.00	N.A.	636.10
MAHARASHTRA/AP BORDER TO ISLAM NAGAR,(NS-2/BOT/AP-6),NH-7	12/2003	360.42	11/2009	360.42	07/2010	478.40
ELEVATED HIGHWAY FROM SILK BOARD JUNCTION TO ELECT	03/2005	450.00	07/2008	450.00	N.A.	876.61
ISLAM NAGAR TO KADTAL	12/2003	546.83	03/2010	546.83	08/2010	667.80
WAINGANGA BRIDGE - CHHATISGARH-MAHARASHTRA	03/2008	424.00	09/2010	424.00	09/2010	298.40
<u>Shipping & Ports</u>						
ACQUISITION OF TWO NOS.OF 470000 DWT MR TANKERS	12/2006	411.32	03/2010	411.32	09/2010	406.28
<u>Telecommunications</u>						
EXP. OF 750K GSM LINES OF 2.5 GSM AND VALIDATION EQU	02/2007	741.77	10/2007	278.16	09/2010	151.37

V. List of projects completed/dropped current month

(Cost /Expenditure in Rs. crore)

Project	DOA	Original		Now anticipated		Final
		Cost	DOC	Cost	DOC	Expenditure
GSM EQUIPMENT OF 1006280 LINES IN TAMILNADU PH-4.5	06/2008	409.21	12/2008	483.54	09/2010	470.24
<u>Steel</u>						
Augmentation of Iron Ore Storage in RMHP	05/2008	480.00	09/2010	480.84	12/2011	4.04
<u>Telecommunications</u>						
COMMISSIONING OF GSM EQUIPMENT OF 650K LINES (PH-	11/2006	364.52	N.A.	364.52	09/2010	51.44
<u>Petroleum</u>						
Construction of Tank and Blending Facility at Vadi	02/2009	267.00	N.A.	267.00	08/2011	72.99
<u>Road Transport & Highways</u>						
DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915	12/2003	300.00	10/2008	300.00	N.A.	.00
<u>Petroleum</u>						
MSQ UPGRADATION PROJECT AT PANIPAT REFINERY	01/2008	1,131.00	12/2009	1,131.00	N.A.	750.71
<u>Steel</u>						
REBUILDING OF COKE OVEN BATTERY-10	03/2007	416.50	09/2009	436.54	08/2010	305.14
<u>Telecommunications</u>						
EXPANSION OF EXISTING 2G&3G GSM N/W BY 750 KPE NO	10/2008	180.53	12/2009	180.53	09/2010	25.97
<u>Petroleum</u>						
LUBE OIL BASE STOCK QUALITY UPGRADATION AT MUMBAI REFINERY	10/2006	638.90	04/2009	1,030.00	07/2010	796.21
DADRI- PANIPAT R-LNG SPUR PIPELINE	06/2005	250.66	06/2008	389.00	07/2010	350.96
<u>Shipping & Ports</u>						
DEV. & OPRATION OF AN INTERNATIONAL CONTAINER TRA	11/2004	2,118.00	11/2004	2,118.00	10/2010	.00
<u>Steel</u>						
COKE OVEN BATTERY NO. 4 PHASE-II	08/2007	108.00	10/2009	168.95	06/2011	12.00
<u>Petroleum</u>						
SINGLE POINT MOORING PROJECT	11/2008	643.46	N.A.	643.46	N.A.	726.45

V. List of projects completed/dropped current month

(Cost /Expenditure in Rs. crore)

Project	DOA	Original		Now anticipated		Final
		Cost	DOC	Cost	DOC	Expenditure
AT VISAKHAPATNAM						
<u>Telecommunications</u>						
NATIONAL RADIO SPECTRUM MANAGEMENTand MONIT. SY. I	08/2000	279.97	12/2004	172.04	09/2010	136.24
<u>Petroleum</u>						
BINA DESPATCH TERMINAL	05/2007	490.71	12/2009	639.11	03/2010	590.52
INST. OF FCC GASOLINE DESULPHUN UNIT AT MATHURA RE	01/2008	348.00	12/2009	348.00	N.A.	186.58

VI. List of projects added

(Cost in Rs. crore)

Project	DOA	Original		Anticipated	
		Cost	DOC	Cost	DOC
<u>Shipping & Ports</u>					
Modification & Strengthening of Existing Berth No. 1 to 6	6/2010	277.00	3/2012	277.00	3/2012
<u>Petroleum</u>					
Fluidized catalytic cracking unit(FCCU) revamp	7/2010	1,000.00	1/2013	1,000.00	1/2013
<u>Power</u>					
Transmission System for phase-1 generation project	9/2010	2,074.86	2/2013	2,074.86	2/2013
<u>Petroleum</u>					
Butadiene Extraction Unit(BDEU) at Panipat	11/2009	341.50	2/2013	342.00	2/2013
<u>Coal</u>					
KARMA OCP	6/2009	162.46	/	162.46	-

VII. Milestones (Cumulative due & achieved)

Total	2191
Achieved up to month	802

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay
	Original	Anticipated	Original	Last month	This month	(in months)
<u>Atomic Energy</u>						
KUDANKULAM APP (NPCIL)	13,171.00	13,171.00	12/2008	06/2011	12/2011	6
<u>Coal</u>						
BHUBANESWARI OCP	490.10	490.10	03/2014	03/2016	03/2017	12
GEVRA EXPANSION OCP (SECL) (25 MTY)	1,667.55	2,675.67	03/2010	03/2012	03/2014	24
BLOCK-B OCP NCL (3.5 MTY)	746.04	437.34	03/2012	03/2013	03/2015	24
<u>Fertilisers</u>						
NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT	1,478.63	1,478.63	N.A.	10/2012	12/2012	2
PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJE	1,292.84	1,292.84	N.A.	10/2012	01/2013	3
BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJ	1,294.19	1,294.19	N.A.	10/2012	01/2013	3
THAL AMMONIA REVAMP PROJECT	488.75	488.75	N.A.	03/2011	11/2011	8
<u>Steel</u>						
INSTALLATION OF 700 TPD OXYGEN PLANT, ROURKELA	302.70	302.70	06/2009	08/2010	10/2010	2
SIMULTANEOUS BLOWING OF BOF CONVERTER OF SMS-II	197.66	197.66	11/2009	08/2010	10/2010	2
EXPANSION OF SALEM STEEL PLANT	1,902.00	1,902.00	06/2011	08/2010	10/2010	2
Rebuilding of coke oven battery No.1 & 2 (Bokaro S	500.90	500.90	04/2010	04/2011	07/2011	3
REBUILDING OF COKE OVEN BATTERY NO-6 (BSP)	172.78	172.78	01/2010	11/2010	02/2011	3
<u>Petroleum</u>						
RESIDUE UPGRADATION AND MS/HSD QUALITY IMPROVEMENT	5,693.00	6,898.00	01/2010	10/2010	11/2010	1
MSQ UPGRADATION PROJECT AT GUWAHATI REFINERY	372.00	325.00	02/2010	09/2010	10/2010	1
MSQ UPGRADATION PROJECT AT BARAUNI REFINERY	1,492.00	1,505.24	04/2010	10/2010	11/2010	1

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
MSQ IMPROVMENT PROJECT	293.60	293.60	12/2009	09/2010	10/2010	1
INSTALLATION OF FCCV AT MUMBAI REFINERY	900.47	900.47	09/2009	10/2010	11/2010	1
CAPACITY EXP. CUM MODERNISATION PH-II	2,591.80	3,941.41	12/2009	09/2010	10/2010	1
BNPL SPURLINE (UTTRANCHAL & PUNJAB)	540.92	540.92	06/2011	05/2011	06/2011	1
DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON	1,431.91	1,676.00	09/2009	10/2010	12/2010	2
MSQ UPGRADATION PROJECT AT DIGBOI REFINERY	356.00	300.00	02/2010	09/2010	11/2010	2
VIJAPUR DADRI-BAWANA PIPE LINE PROJECT	5,595.31	3,700.00	11/2009	08/2010	10/2010	2
SULTANPUR NEEMRANA PIPE LINE PROJECT (Spurline to CJPL)	396.13	396.13	10/2009	09/2010	11/2010	2
ADDITIONAL GAS PROCESSING UNITS AT URAN	1,797.35	1,797.35	12/2011	11/2012	01/2013	2
CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI	224.00	224.00	12/2010	12/2010	02/2011	2
COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I	1,512.00	1,434.00	04/2011	10/2010	04/2011	6
Power						
NORTHERN REGION SYSTEM STRENGTHENING SCHEME-IX	525.14	525.14	07/2011	07/2011	10/2010	-9
TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP	297.37	297.37	07/2011	07/2011	12/2010	-7
NORTHERN REGION SYSTEM STRENGTHENING- XI	417.76	417.76	12/2010	12/2010	10/2010	-2
NORTHERN REGION SYSTEM STRENGTHENING SCHEME-X	408.36	408.36	12/2010	12/2010	10/2010	-2
NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XII	261.55	261.55	11/2010	11/2010	10/2010	-1
KORBA STPP STAGE-III	2,448.50	2,448.49	02/2010	10/2010	11/2010	1
WESTERN REGION STRENGTHENING SCHEME-VI	340.72	340.72	11/2010	11/2010	12/2010	1
WESTERN REGION STRENGTHENING SCHEME- IX	230.89	230.89	01/2011	01/2011	02/2011	1
VINDHYACHAL STTP STAGE-IV (NTPC)	5,915.00	5,915.00	11/2012	11/2012	12/2012	1

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
RIHAND STTP STAGE-III (2X500MW) (NTPC)	6,230.81	6,230.81	11/2012	11/2012	12/2012	1
BARH STPP STAGE -II (NTPC)	7,341.04	7,341.04	08/2013	08/2013	10/2013	2
TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.)	3,779.46	3,725.13	09/2009	12/2010	03/2011	3
TEHRI PUMPED STORAGE PLANT(1000MW)	1,657.00	3,124.76	07/2010	12/2014	03/2015	3
TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB G	290.49	299.08	04/2010	09/2010	12/2010	3
EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER	262.10	262.10	09/2010	09/2010	12/2010	3
BARH STPP(3X660MW) NTPC	8,692.97	8,692.97	11/2010	04/2014	09/2014	5
KUNADANKULAM-APP TRANS. SYSTEM (PGCIL)	1,779.29	2,159.07	11/2008	09/2011	03/2012	6
NIMOO BAZGO HYDROELECTRIC PROJECT (NHPC)	611.01	611.02	08/2010	12/2010	07/2011	7
CHAMERA,STAGE-III (NHPC)	1,405.63	1,405.63	08/2010	12/2010	08/2011	8
LOWER SUBANSIRI H.E.P (NHPC)	6,285.33	7,451.99	09/2010	12/2012	12/2013	12
TEESTA LOW DAM HEP, STAGE-IV (NHPC)	1,061.38	1,061.38	09/2009	08/2011	08/2012	12
KOTESHWAR HEP(THDC)	1,301.56	2,398.39	04/2005	12/2010	03/2012	15
RAMPUR HEP(412 MW)	2,047.03	2,047.03	01/2012	03/2012	09/2013	18
<u>Railways</u>						
JIND-SONEPAT (NL),NR	190.81	234.45	N.A.	03/2012	12/2012	9
CHANDIGARH- LUDHIANA(NEW BG LINE),NR	248.44	1,103.47	N.A.	12/2011	12/2012	12
UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	325.00	369.90	03/2010	12/2011	12/2012	12
MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP	5,300.00	5,300.00	03/2014	03/2014	03/2015	12
TALCHER- BIMALAGARH(NL)(ECOR)	726.96	810.78	N.A.	02/2011	03/2012	13
<u>Road Transport & Highways</u>						
HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 293.4-3	239.19	239.19	09/2009	09/2010	10/2010	1
LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7	263.17	263.17	09/2009	09/2010	10/2010	1

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
COCHIN PORT, NH-47 (PORT CONNECTIVITY) KMS 348 - KMS 358	106.00	193.00	08/2006	08/2010	10/2010	2
GORAKHPUR-AYODHYA (LMNHP-4),NH-28, KM.164.00 TO KM.135.00	205.00	205.00	10/2008	10/2010	12/2010	2
AYODHYA-LUCKNOW (LMNHP-3),NH-28, KM.135.000 TO KM.93.075	212.00	212.00	10/2008	10/2010	12/2010	2
JALANDAR-AMRITSAR, KM.407/100 TO KM.456/100, NH-1	263.00	263.00	02/2009	08/2010	10/2010	2
MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B	629.00	629.00	11/2010	09/2010	11/2010	2
HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 376-418	205.92	205.92	08/2009	08/2010	10/2010	2
BANGALORE-NEELAMANGLALA NH-4	445.00	445.00	07/2010	08/2010	10/2010	2
AMRITSAR-WAGHA BORDER	205.88	205.88	06/2010	08/2010	10/2010	2
HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4)	318.00	207.56	08/2004	09/2010	12/2010	3
CHENNAI BYPASS (NHAI) OTHERS, NH-45, 4 & 5	480.00	480.00	11/2007	08/2010	11/2010	3
GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00	227.00	227.00	10/2008	03/2011	06/2011	3
ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0	340.68	340.68	03/2008	12/2010	03/2011	3
NAGAON BYPASS (NH-37)(NHAI)	230.00	230.00	06/2008	09/2010	12/2010	3
FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	332.94	332.94	09/2008	03/2011	06/2011	3
KOTA BYPASS,RJ-4, NH-76 (NHAI)	275.00	250.39	10/2008	09/2010	12/2010	3
LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI)	225.00	225.00	10/2008	12/2010	03/2011	3
RINGBUNDS TO JHAJHANPUR (BR-6)	340.00	340.00	06/2008	12/2010	03/2011	3
SITAPUR-LUCKNOW	322.00	322.00	06/2009	12/2010	03/2011	3
BARA TO ORAI, NH-2, 25	465.00	465.00	04/2009	12/2010	03/2011	3
GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID	600.24	600.24	10/2009	03/2011	06/2011	3
GWALIOR BYPASS, NH-75,3	300.93	300.93	10/2009	10/2010	01/2011	3
GWALIOR-JHANSI, NH-75	604.00	604.00	12/2009	12/2010	03/2011	3
PONDICHERY - TINDIVANAU NH-66	285.00	285.00	07/2010	10/2010	01/2011	3

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2)	367.49	367.49	03/2005	12/2010	04/2011	4
MADURAI -KANIAKUMARI SECTION (NS-41/TN) NH- 7,KM.80 TO KM.120	323.36	323.36	03/2008	08/2010	12/2010	4
NEW MANGALORE PORT NH-17 AND 48	196.50	196.50	06/2008	08/2010	12/2010	4
HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4)	241.00	196.65	08/2004	07/2010	12/2010	5
ORAI TO JHANSI (UP-4),NH- 25, KM.170.0 TO KM.104.0	451.97	451.97	04/2008	10/2010	03/2011	5
KASIA TO GORAKHPUR (NH- 28)(NHAI)	242.00	242.00	12/2008	12/2010	05/2011	5
KURALI-KIRATPUR, NH-21	309.00	309.00	06/2010	10/2010	03/2011	5
SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68	941.00	941.00	01/2011	01/2011	06/2011	5
ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH)	295.00	295.00	08/2010	12/2010	05/2011	5
HALDIA PORT (PORT CONNECTIVITY) (NH-41)	273.00	522.00	03/2005	09/2010	03/2011	6
GAGODHAR- GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254	412.78	479.54	11/2007	06/2010	12/2010	6
UP/BIHAR BORDER TO KASIA (NH-28)(NHAI)	227.00	227.00	12/2008	12/2010	06/2011	6
JHANSI TO LALITPUR, NH- 25,26	355.06	355.06	09/2009	09/2010	03/2011	6
JHANSI TO LALITPUR, NH-26	276.09	276.09	09/2009	09/2010	03/2011	6
TRICHY - KORUR NH-67	516.00	516.00	07/2010	12/2010	06/2011	6
LANKA TO DABOKA (NH- 54)(NHAI)	225.00	225.00	06/2008	08/2010	03/2011	7
SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI)	151.30	151.30	10/2008	03/2011	11/2011	8
GANJAM-ICCHAPURUM,NH- 5(NHAI)	263.27	263.27	02/2004	06/2010	04/2011	10
NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	557.00	557.00	02/2010	12/2010	10/2011	10
DARBHANGA- MUZAFFARPUR, NH-57 (NHAI)	305.00	305.00	06/2008	12/2010	11/2011	11
MAIBANG TO LUNDING (AS- 24), KM.111.000 TO KM.126.450	155.04	155.04	11/2008	12/2012	12/2013	12
SAGAR - RAJMARG CHORAH, KM 211 TO KM 255, NH-26 (NHAI)	203.43	203.43	10/2008	12/2010	12/2011	12

VIII. List of projects reporting additional delays



Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54	212.00	212.00	09/2007	12/2012	12/2013	12
HARANGAJO TO MAIBANG, NH-54	196.00	196.00	07/2009	12/2012	12/2013	12
AGRA-BYPASS(NS-1/UP- 1), KM 176.8-13.03 NH-2,3	348.16	348.16	09/2007	02/2011	06/2013	28
MAIBANG TO LUNDING (AS- 25), KM.83.400 TO KM.111.000	199.81	199.81	04/2009	12/2010	12/2013	36
MAIBANG TO LUNDING (AS- 26), KM.60.500 TO KM.83.400, NH-54	167.64	167.64	11/2008	12/2010	12/2013	36
<u>Shipping & Ports</u>						
DEEPENING OF CHEENEL AT PARADIP PORT	154.84	253.36	06/2007	09/2010	12/2010	3
ACQUISITION OF 2 NOS. OF 105000 DWT LR-II TANKERS	586.58	586.58	11/2010	11/2010	03/2011	4
<u>Telecommunications</u>						
GSM equipment of 2,00,000Lines (2G) Rajasthan (Ph	577.35	577.35	09/2010	08/2010	09/2010	1
GSM equipment of 900000Lines (2G) PunjabPhase V.2	241.49	241.49	09/2009	09/2010	11/2010	2
GSM equipment of 849862Lines (2G) 150138 lines 3(G	584.33	584.33	02/2009	08/2010	10/2010	2
GSM equipment of 799000Lines (2G) 101000 lines 3(G	328.13	392.44	03/2009	08/2010	10/2010	2
GSM equipment of 1900000Lines (2G) 335500lines 3(G	848.70	848.70	01/2010	09/2010	11/2010	2
Expn of existing 2G & 3G GSM N/W by 750k	180.53	180.53	06/2010	09/2010	12/2010	3
GSM equipment of 200000Lines (2G) UP(West)Phase V.	336.84	336.84	10/2009	08/2010	11/2010	3
GSM equipment of 975000Lines (2G) 325000 lines 3(G	625.53	625.53	02/2010	08/2010	11/2010	3
GSM equipment of 1100000Lines (2G) UP East Phase	624.75	624.75	09/2010	08/2010	11/2010	3
GSM equipment of 1867000Lines (2G) 383000 lines 3(	868.00	868.00	08/2009	09/2010	12/2010	3



VIII. List of projects reporting additional delays



Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
GSM equipment of 1625000Lines (2G) 325000 lines 3(	916.70	916.70	11/2010	08/2010	11/2010	3
GSM equipment of 1900000Lines (2G) 401700 lines 3(	760.20	810.37	01/2010	08/2010	11/2010	3
GSM equipment of 1700000Lines (2G) 234100 lines 3(	677.75	719.70	10/2009	09/2010	12/2010	3
GSM equipment of 375000Lines (2G) 75000lines 3(G)	170.23	167.20	06/2009	08/2010	12/2010	4
GSM equipment of 945000Lines (2G) 225000lines 3(G)	366.00	529.32	10/2008	08/2010	12/2010	4
GSM equipment of 1500000Lines (2G) 264700lines 3(G)	922.91	922.91	01/2010	08/2010	12/2010	4
GSM equipment of 614000Lines (2G) 150000lines 3(G)	315.19	315.19	01/2010	08/2010	12/2010	4
<u>Urban Development</u>						
DELHI MRTS PHASE-II PROJECT	8,676.00	18,894.36	06/2010	09/2010	10/2010	1



Number of projects reporting additional delay = 127



Sector wise Trend and Graphical Analysis (June'10 ,July'10,Aug'10,Sep'10)

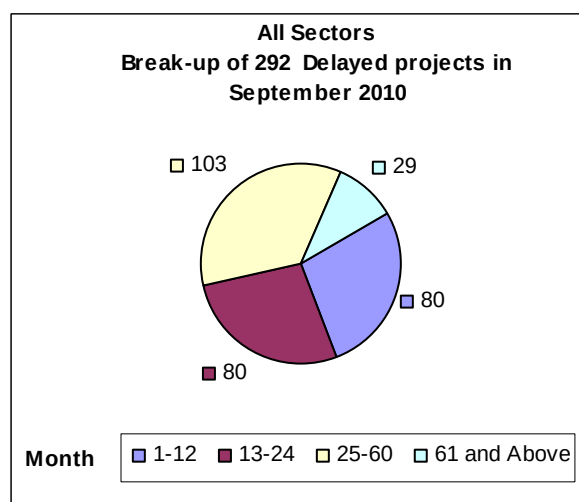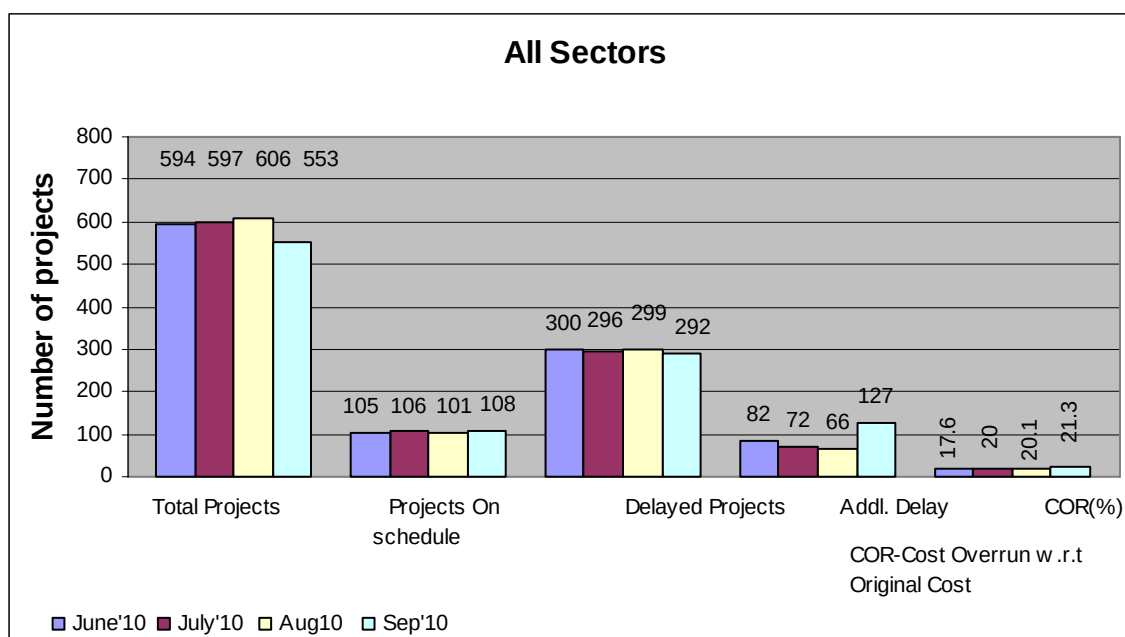

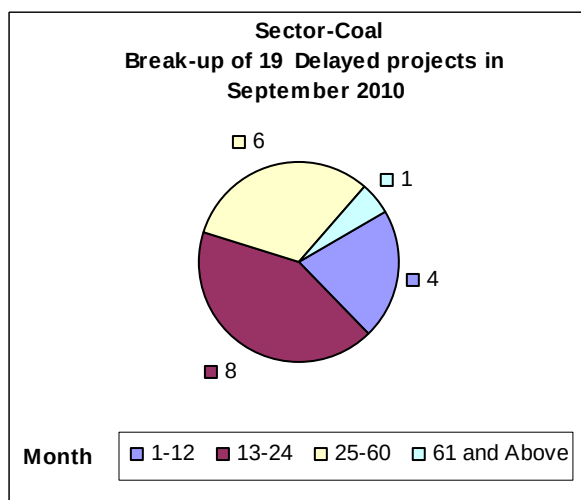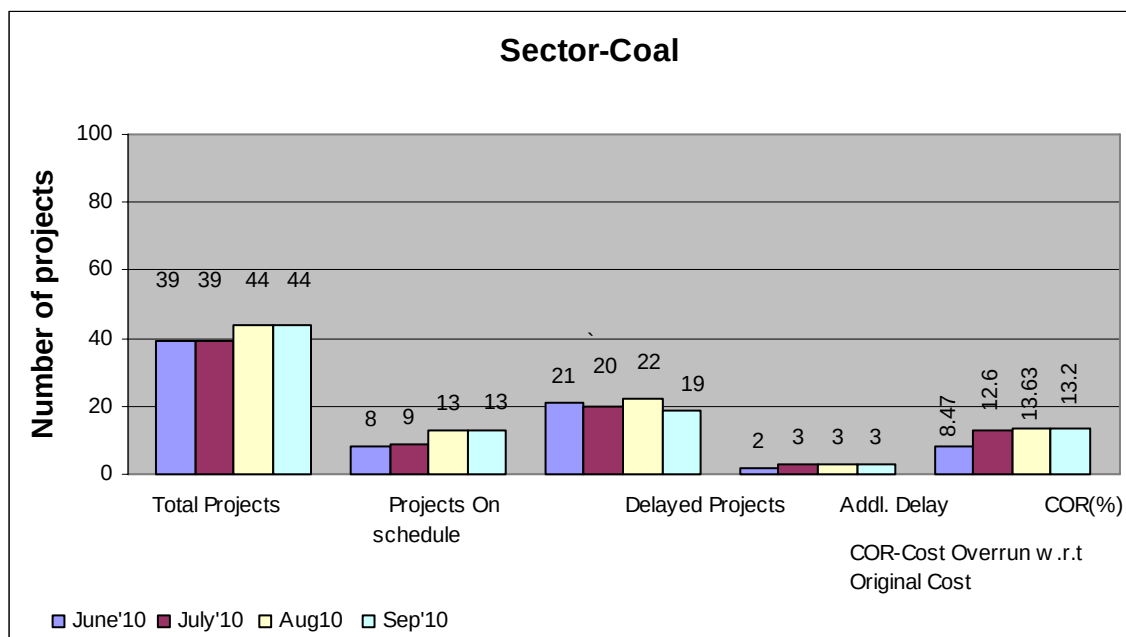


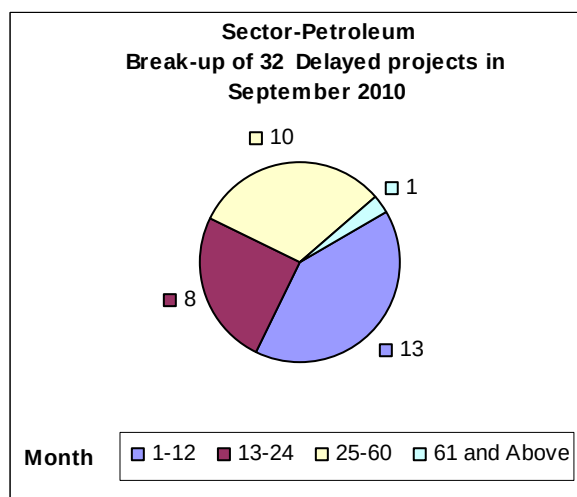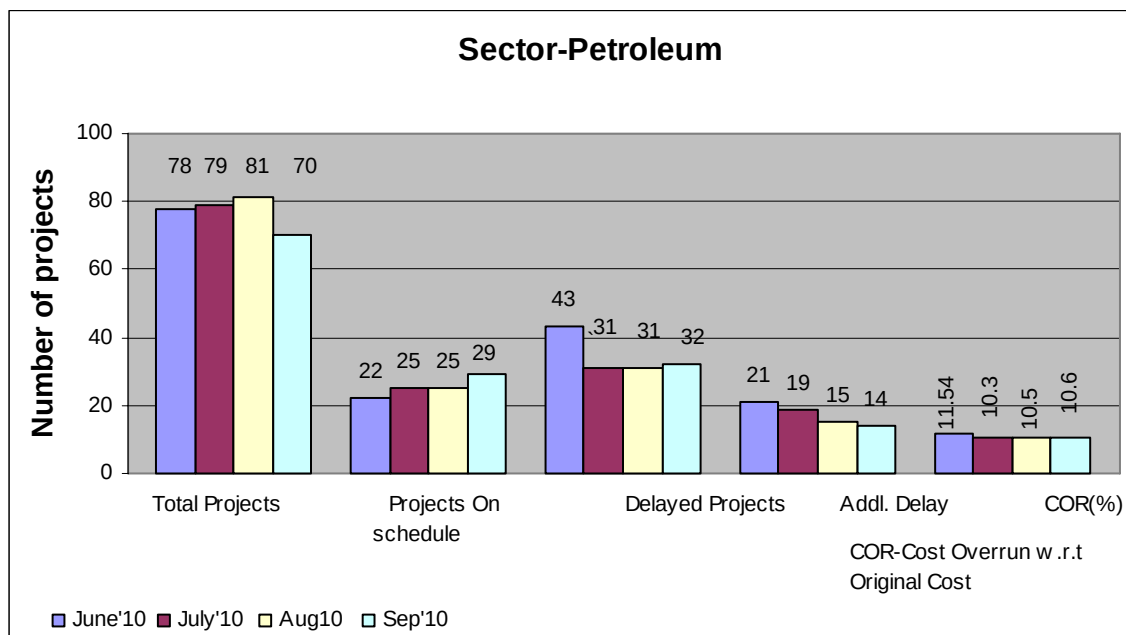

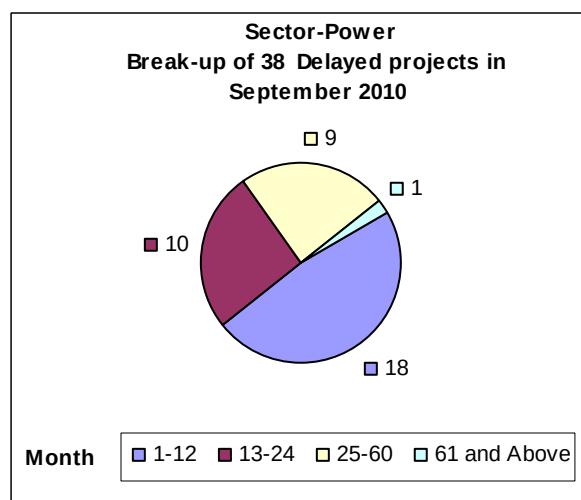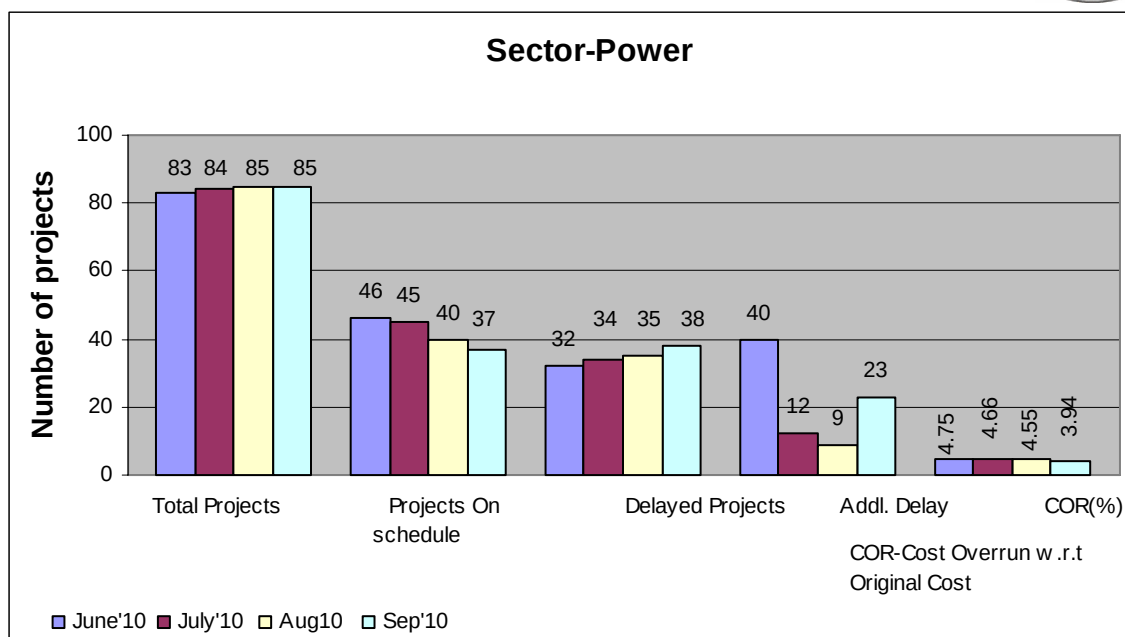


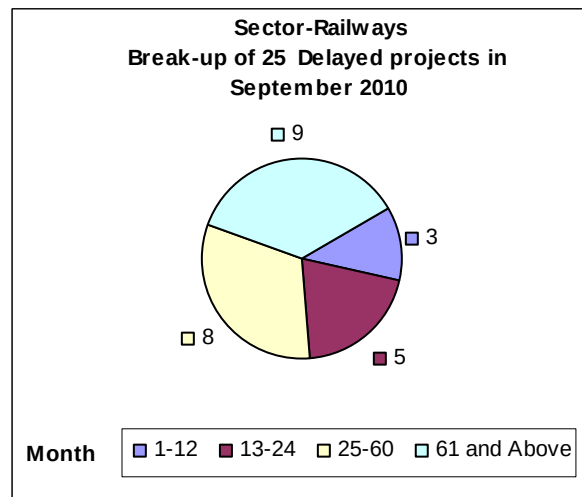
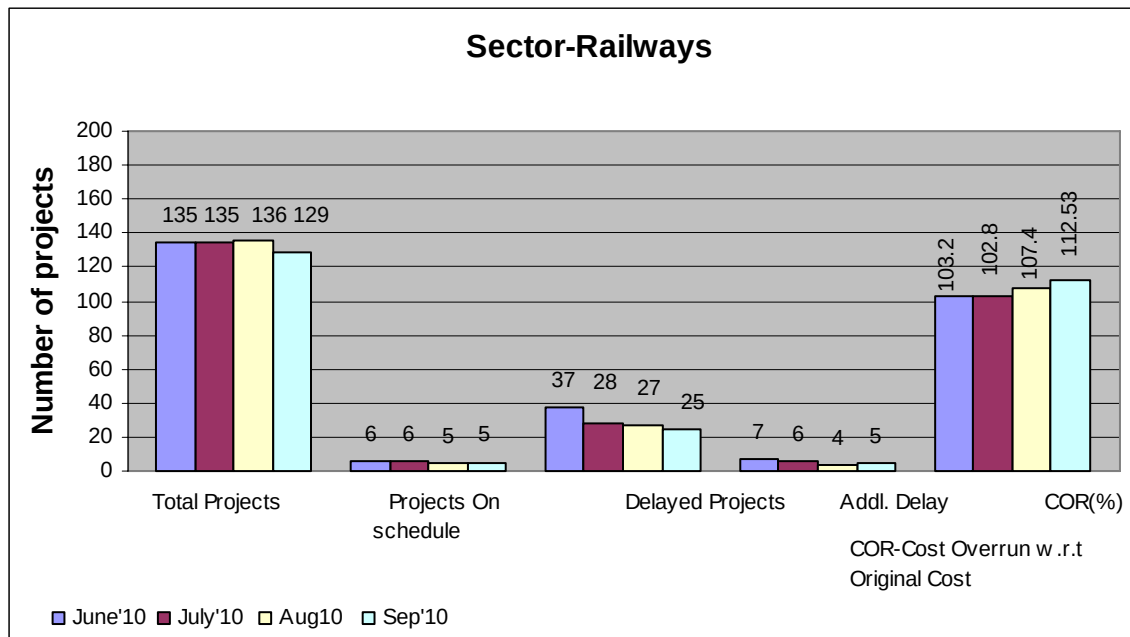




Sector-Road Transport and Highways


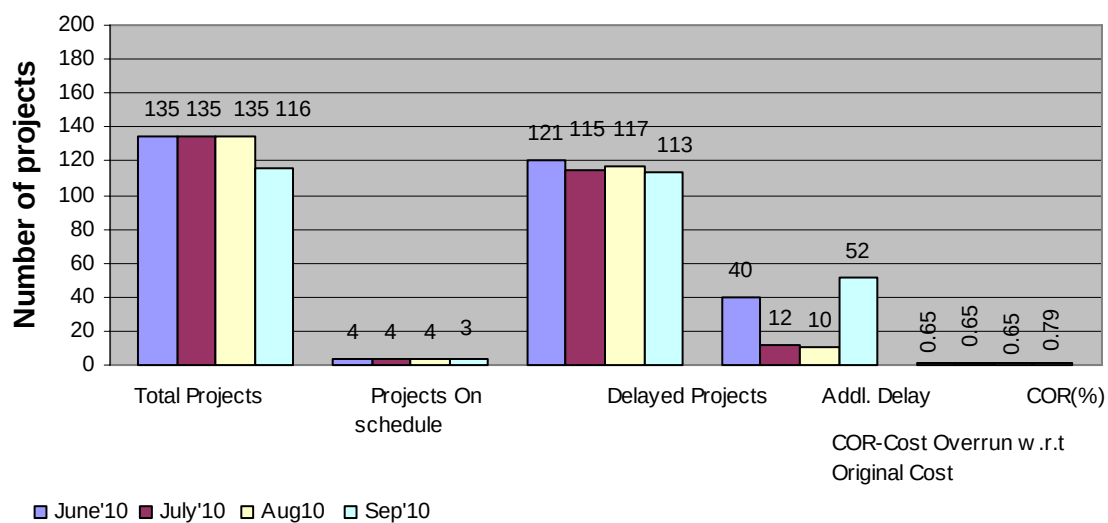


Sector-Road Transport and Highways Break-up of 113 Delayed projects in September 2010

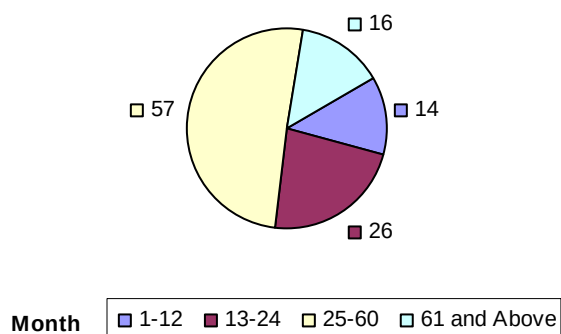

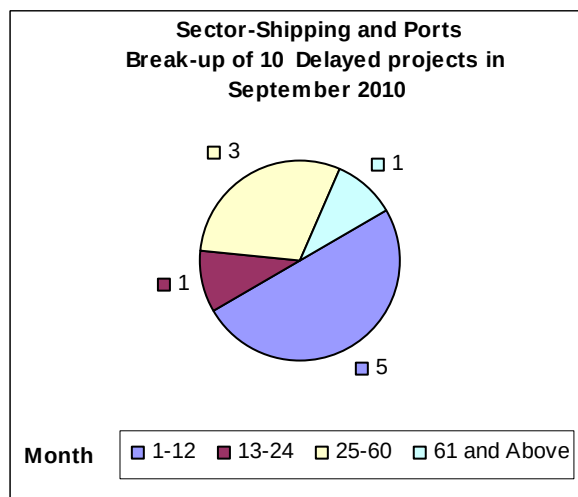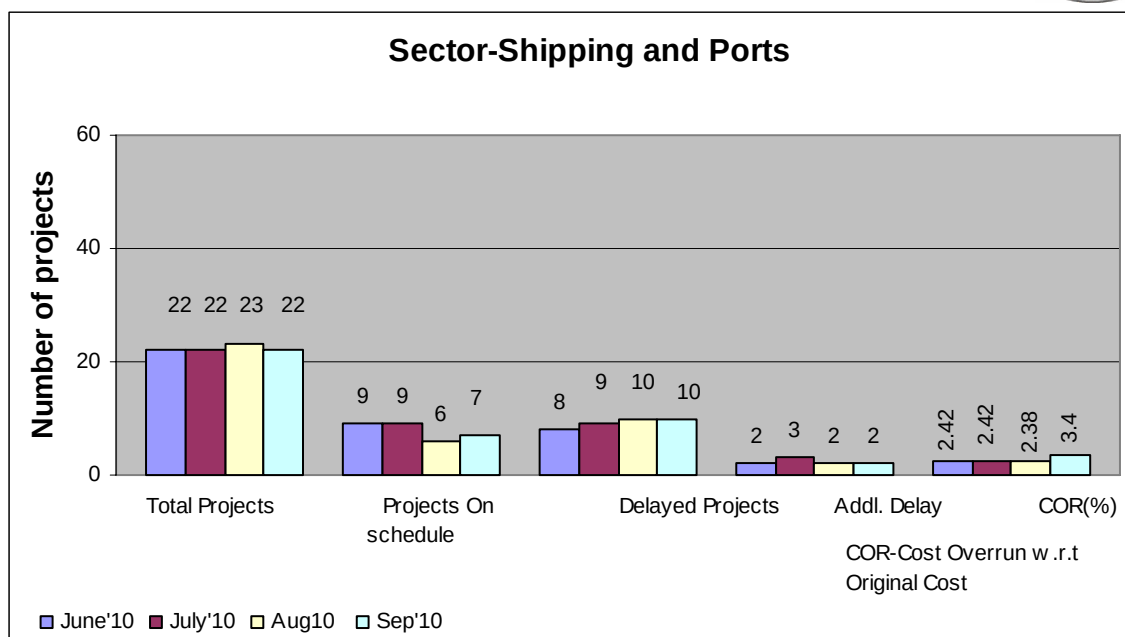

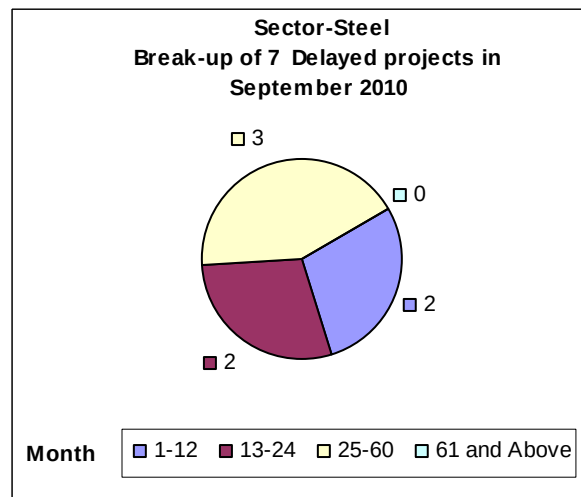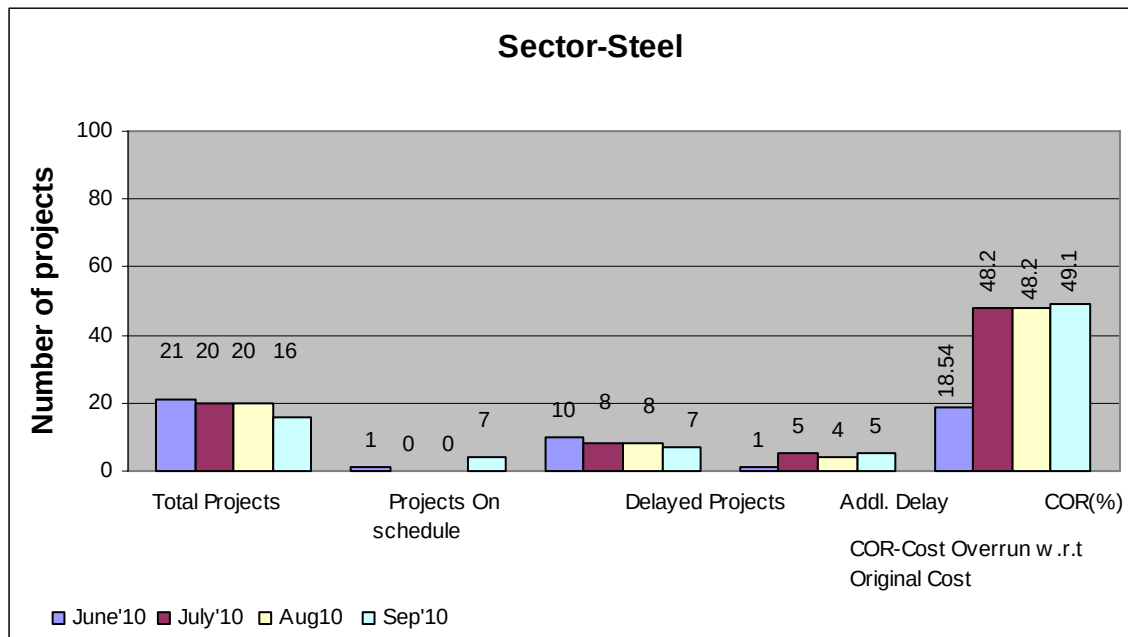

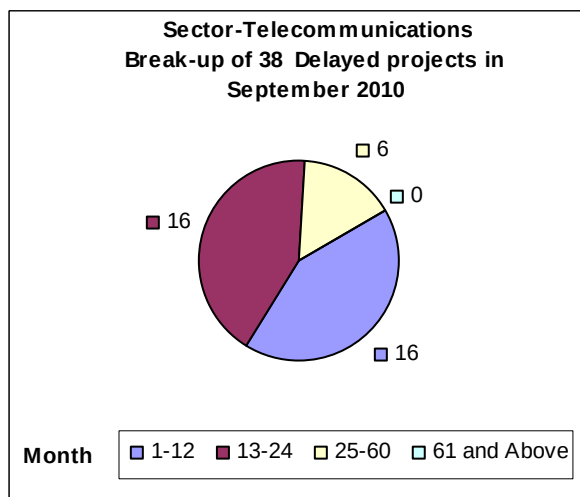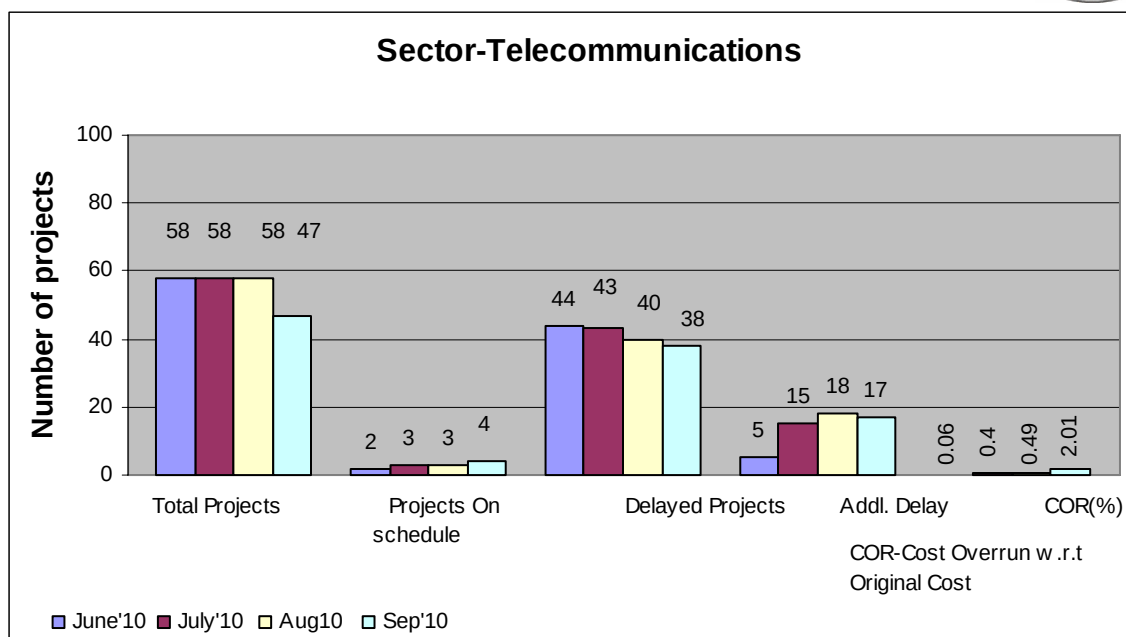

Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)		
		Original	Latest	Anticipated
Atomic Energy	4	21,982.29	21,982.29	23,236.29
Civil Aviation	9	5,347.40	5,347.40	5,347.40
Coal	44	25,210.30	28,502.92	28,542.19
Fertilisers	6	5,317.41	5,317.41	5,317.41
Mines	1	4,091.51	4,401.76	4,401.76
Steel	16	43,096.53	58,618.46	64,258.46
Petroleum	70	144,690.62	158,113.41	160,094.89
Power	85	180,925.92	181,844.97	188,054.62
Health & Family Welfare	1	71.18	422.60	443.15
Railways	129	49,023.84	60,489.90	104,193.13
Road Transport & Highways	116	34,200.81	34,200.81	34,474.24
Shipping & Ports	22	17,128.49	17,227.01	17,711.75
Telecommunications	47	22,779.47	22,866.14	23,237.57
Urban Development	2	15,071.00	15,000.36	30,503.36
Water Resources	1	542.90	542.90	1,187.00
Grand total	553	569,479.67	614,878.34	691,003.22

(Sep,2010)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Atomic Energy</u>									
1	KAIGA 3 and 4 UNITS (NPCIL) - [020100041]NPCIL,Karnataka	05/2001	4,213.00	3,282.00	2,572.00	10/2009 09/2007	12/2010	39(R1)	71/75
2	URANIUM ORE MINE & PROCESSING PLANT AT TUMMALAPALL - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29	1,106.29	778.60	-	04/2011	-	0/1
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00	5,677.00	2,592.29	09/2010	09/2011	12(O)	8/80
4	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00	13,171.00	13,150.00	12/2008	12/2011	36(O)	61/119
Total			21,982.29	23,236.29	19,092.89				140/275
<u>Civil Aviation</u>									
5	CONSTRUCTION OF RCC/PRE STRESSD CONCRETE BRIDGE K3 - [N04000068]AAI,Tamil Nadu	06/2009	213.35	213.35	153.05	09/2010	11/2010	2(O)	0/0
6	D/O OF TERMINAL BLDG. AND PAVEMENT WORKS AT CHENNA - [N04000040]AAI,Tamil Nadu	01/2008	535.00	535.00	331.80	06/2010	12/2010	6(O)	0/0
7	D/O KAMARAJ DOMESTIC TER-PH-II & EXP. ANNA INT. TE(K1) - [N04000038]AAI,Tamil Nadu	08/2008	1,273.00	1,273.00	594.84	01/2011	01/2011	0(O)	0/0
8	Extension of Secondary Runway(K2) - [N04000056]AAI,Tamil Nadu	08/2008	230.00	230.00	188.12	01/2011	01/2011	0(O)	0/0
9	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51	1,942.51	860.83	05/2011	08/2011	3(O)	0/0
10	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	204.73	204.73	5.97	05/2012	05/2012	0(O)	0/0
11	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BLDG. A - [N04000017]AAI,Gujarat	02/2007	290.92	290.92	185.74	-	-	-	1/24
12	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	264.29	264.29	-	01/2011	-	-	0/0
13	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	393.60	393.60	202.26	06/2013	-	-	0/0
Total			5,347.40	5,347.40	2,522.61				1/24
<u>Coal</u>									
14	BARSINGSAR TPS (2X125MW) (NLC) - [060100089]NLC,Rajasthan	12/2004	1,114.18	1,626.09	1,488.75	06/2009	10/2010	16(O)	59/26
15	BALRAM OCP EXTENSION - [N06000044]JMCL,Orissa	12/2007	172.08	172.08	485.97	03/2009 03/2010	03/2011	12(R3)	0/0
16	Churi Benti UG - [N06000083]CCL,Jharkhand	06/2007	163.51	163.51	33.46	03/2011	03/2011	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
17	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 2,453.57	2,453.57	2,025.08	06/2009 -	06/2011	24(O)	41/24
18	KULDA OCP (MAHANADI COALFIELDS LTD.) - [060100092]MCL,Orissa	01/2005	302.96 -	302.96	64.16	03/2010 03/2012	03/2012	0(R3)	0/4
19	ASHOK EXPN.OCP -CCL (5 MTY) - [060100096]CCL,Jharkhandd	04/2006	471.66 341.63	341.63	101.85	03/2011 03/2012	03/2012	0(R3)	0/0
20	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03 -	249.03	37.64	03/2012 -	03/2012	0(O)	8/42
21	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40 -	259.40	0.87	03/2012 -	03/2012	0(O)	0/0
22	ANANTA OC EXPANSION PH-III - [N06000067]MCL,Orissa	08/2008	207.28 -	207.28	262.78	03/2012 -	03/2012	0(O)	0/0
23	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.57 418.97	418.97	66.32	03/2012 -	03/2012	0(O)	7/27
24	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.91 -	181.19	0.07	- -	03/2012	-	2/34
25	North Urimari OCP - [N06000084]CCL,Jharkhandd	12/2007	179.87 -	179.87	68.36	03/2012 -	03/2012	0(O)	0/0
26	Tapin OCP - [N06000086]CCL,Jharkhandd	08/2008	264.68 -	264.68	71.93	03/2012 -	03/2012	0(O)	0/0
27	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	09/2006	212.34 779.26	779.26	124.02	03/2013 07/2012	07/2012	0(R3)	2/22
28	TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 -	4,904.54	1,071.67	08/2012 -	08/2012	0(O)	0/0
29	KAKATIYA LAONGWALL - [N06000048]SCCL,Andhra Pradesh	12/2008	453.63 -	453.63	50.77	- 12/2012	12/2012	0(R3)	7/44
30	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Madhya pradesh	05/2006	789.88 741.56	741.56	136.37	03/2010 03/2013	03/2013	0(R3)	0/1
31	KUSMUNDA EXPN.OCP(SECL)(10MTY) - [N06000008]SECL,Chhatisgarh	06/2006	737.65 1,188.31	1,188.31	554.36	03/2011 03/2013	03/2013	0(R3)	0/4
32	MAGADH OC (CCL) - [N06000015]CCL,Jharkhandd	07/2006	469.78 706.40	706.40	16.23	07/2012 03/2013	03/2013	0(R3)	0/1
33	BINA EXTN. PROJ - [N06000019]NCL,Multi State	11/2006	168.97 168.97	168.97	139.77	03/2014 03/2013	03/2013	0(R3)	1/1
34	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	03/2013	467.78 -	467.78	11.42	- -	03/2013	-	0/83
35	KANIHA OCP - [N06000035]MCL,Multi State	12/2007	457.77 -	457.77	52.04	- -	03/2013	-	0/2
36	HINGULA OC-II EXP. PH-II (15 MTY) - [N06000068]MCL,Orissa	11/2008	475.93 479.53	479.53	212.86	03/2013 -	03/2013	0(O)	0/0
37	Purnadih OCP - [N06000085]CCL,Jharkhandd	07/2008	210.98 -	210.98	20.05	03/2013 -	03/2013	0(O)	0/0
38	GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093]SECL,Chhatisgarh	07/2005	1,667.55 2,675.67	2,675.67	1,011.42	03/2010 03/2014	03/2014	0(R3)	3/7
39	DIPKA EXPANSION OCP (SECL) (20 MTY) - [060100094]SECL,Chhatisgarh	07/2005	1,268.53 1,943.66	1,943.66	887.83	03/2010 03/2014	03/2014	0(R3)	2/6

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
40	CHURCHA UG - [N06000046]SECL, Chhatisgarh	06/2008	462.35	462.35	259.73	06/2014 03/2014	03/2014	0(R3)	0/0
41	RAJMAHAL OC EXP. - [N06000056]ECL,	02/2006	50.08 153.82	153.82	14.77	- 03/2014	03/2014	0(R3)	0/1
42	PENGANGA OC - [N06000066]WCL, Andhra Pradesh	10/2008	339.77	339.77	0.52	- -	03/2014	-	0/1
43	KARTALI (EAST) OC - [N06000076]SECL, Chhatisgarh	07/2008	178.44	178.44	-	03/2014 -	03/2014	0(O)	0/0
44	MANIKPUR OC EXPANTION - [N06000081]SECL, Chhatisgarh	11/2009	321.42 321.50	321.50	211.81	03/2013 03/2014	03/2014	0(R3)	0/0
45	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL, Madhya Pradesh	06/2006	746.04 437.34	437.34	136.70	03/2012 03/2015	03/2015	0(R3)	0/1
46	JHANJRA LONGWAL UG PHASE II - [N06000020]ECL, West Bengal	11/2006	287.18	287.17	-	11/2009 -	03/2015	64(O)	0/0
47	GOPAL PRASAD OCP - [N06000042]MCL, Orissa	02/2008	395.87	395.87	24.33	03/2013 03/2015	03/2015	0(R3)	0/0
48	PELMA OC - [N06000045]SECL, Chhatisgarh	07/2008	448.32	448.32	-	03/2012 03/2015	03/2015	0(R3)	0/0
49	Batura OC - [N06000049]BCCL, Madhya Pradesh	09/2008	203.82	203.82	-	03/2013 03/2015	03/2015	0(R3)	0/0
50	JAGANNATHPOR OC - [N06000075]SECL, Chhatisgarh	09/2008	152.43	152.43	-	03/2015 -	03/2015	0(O)	0/0
51	RKP OCP PHASE-I - [N06000079]SCCL, Uttaranchal	03/2010	201.58 209.78	209.78	0.18	- -	03/2015	-	0/31
52	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]NCL, Madhya Pradesh	05/2006	1,352.04 1,143.54	1,143.54	32.03	03/2014 03/2016	03/2016	0(R3)	1/1
53	TALABIRA OCP - [N06000043]MCL, Orissa	03/2008	447.72	447.72	6.04	03/2015 03/2016	03/2016	0(R3)	0/0
54	AMLAI OC EXPANSION SECTOR 'B' (1.50 MTY) - [N06000082]SECL, Chhatisgarh	11/2009	158.59	198.59	91.68	03/2016 -	03/2016	0(O)	0/0
55	Rajrappa RCE OCP - [N06000087]JCL, Jharkhand	12/2009	510.85	510.85	290.79	03/2016 -	03/2016	0(O)	0/0
56	BHUBANESWARI OCP - [N06000034]MCL, Orissa	12/2007	490.10	490.10	58.77	03/2014 03/2017	03/2017	0(R3)	0/0
57	KARMA OCP - [N06000088]CCL, Jharkhand	06/2009	162.46	162.46	-	- -	-	-	0/0
Total			25,210.30	28,542.19	10,123.40				133/363
Fertilisers									
58	CAPACITY ENHANCEMENT OF VIJAI PUR-I PLANTS - [N08000007]NFL, Madhya Pradesh	09/2008	325.00	325.00	-	07/2011 -	07/2011	0(O)	0/0
59	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL, Madhya Pradesh	09/2008	438.00	438.00	-	07/2011 -	07/2011	0(O)	0/0
60	THAL AMMONIA REVAMP PROJECT - [N08000003]RCF,	01/2009	488.75	488.75	28.66	- 11/2011	11/2011	0(R3)	2/22
61	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL, Punjab	01/2010	1,478.63	1,478.63	43.41	- -	12/2012	-	0/8

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
62	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJE - [N08000004]NFL,Haryana	01/2010	1,292.84	1,292.84	46.98	-	01/2013	-	0/5
63	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJ - [N08000005]NFL,Punjab	01/2010	1,294.19	1,294.19	42.93	-	01/2013	-	0/5
	Total		5,317.41	5,317.41	161.98				2/40
	Mines								
64	SECOND PHASE EXPANSION OF CAPTIVE ALUMINIUM,SMELTER AND POWE - [100100054]NALCO,Orissa	10/2004	4,091.51	4,401.76	3,856.50	12/2008 01/2011	03/2011	2(R3)	116/110
	Total		4,091.51	4,401.76	3,856.50				116/110
	Steel								
65	REBUILDING OF BLAST FURNANCE NO.2(BOKARO STEEL PL - [N12000035]SAIL,Jharkhandd	10/2007	892.32	892.32	616.57	08/2009	07/2010	11(O)	2/1
66	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00	353.00	188.89	02/2010	08/2010	6(O)	0/0
67	INSTALLATION OF 700 TPD OXYGEN PLANT, ROURKELA - [N12000025]SAIL,Orissa	07/2007	302.70	302.70	242.30	06/2009	10/2010	16(O)	0/0
68	SIMULTANEOUS BLOWING OF BOF CONVERTER OF SMS-II - [N12000036]SAIL,Orissa	01/2008	197.66	197.66	128.68	11/2009	10/2010	11(O)	0/0
69	EXPANSION OF SALEM STEEL PLANT - [N12000050]SAIL,Tamil Nadu	01/2008	1,902.00	1,902.00	1,694.98	06/2011	10/2010	-8(O)	2/6
70	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00	358.00	114.32	02/2010	01/2011	11(O)	0/0
71	REBUILDING OF COKE OVEN BATTERY NO-6 (BSP) - [N12000054]SAIL,Jharkhandd	07/2008	172.78	172.78	108.46	01/2010	02/2011	13(O)	0/1
72	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]SAIL,Madhya pradesh	07/2007	111.28 232.93	232.93	74.57	05/2011	05/2011	0(O)	0/1
73	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00	12,228.00	7,323.00	10/2009	06/2011	20(O)	4/126
74	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00	14,443.00	8,898.53	06/2011	06/2011	0(O)	0/6
75	Rebuilding of coke oven battery No.1 & 2 (Bokaro S - [N12000033]SAIL,Jharkhandd	10/2007	500.90	500.90	216.39	04/2010	07/2011	15(O)	0/2
76	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhandd	01/2008	3,316.00 6,325.00	6,325.00	1,313.20	12/2011 12/2011	12/2011	0(R3)	0/7
77	EXPENSION OF ROURKELA STEEL PLANT - [N12000056]SAIL,Orissa	09/2008	6,133.00	8,128.00	2,506.34	02/2011	03/2013	25(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
78	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	5,185.00 17,265.00	17,265.00	1,488.41	03/2013 03/2013	03/2013	0(R3)	0/8
79	Deve. of Bailadila Iron Ore Deposit-II(B)(NMDC) - [N12000018]NMDC,Andhra Pradesh	01/2003	295.89 607.17	607.17	233.52	- -	-	-	2/21
80	POWER PLANT-I - [N12000039]RINL,Andhra Pradesh	09/2007	462.00 -	350.00	84.40	12/2009 -	-	-	0/0
	Total		43,096.53 -	64,258.46	25,232.56				10/179
Petroleum									
81	INST. OF FACILITIES FOR IMPROVEMENT IN DIESEL QUALITY (IOCL) - [160100289]IOCL,West Bengal	11/2005	1,876.00 2,869.00	3,155.00	2,747.34	04/2009 12/2009	02/2010	2(R1)	41/36
82	C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC) - [160100168]ONGC,Gujarat	12/2003	900.92 -	1,493.49	726.23	06/2006 07/2010	10/2010	3(R3)	0/2
83	EXPANSION OF PANIPAT REFINERY FROM 12 TO 15 MMTPA - [N16000017]IOCL,	06/2005	806.00 -	1,096.23	809.69	03/2008 12/2009	10/2010	10(R1)	18/66
84	MSQ UPGRADEATION PROJECT AT GUWAHATI REFINERY - [N16000036]IOCL,Assam	04/2008	372.00 -	325.00	222.87	02/2010 -	10/2010	8(O)	0/0
85	MSQ IMPROVMENT PROJECT - [N16000040]BRPL,Assam	04/2008	293.60 -	293.60	-	12/2009 -	10/2010	10(O)	0/0
86	VIJAPUR DADRI-BAWANA PIPE LINE PROJECT - [N16000048]GAIL,Multi State	11/2007	5,595.31 4,262.00	3,700.00	3,260.61	11/2009 04/2010	10/2010	6(R3)	0/0
87	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	281.07	1.13	10/2010 -	10/2010	0(O)	0/0
88	CAPACITY EXP. CUM MODERNISATION PH-II - [N16000080]BPCL,Kerala	09/2009	2,591.80 3,941.41	3,941.41	2,864.54	12/2009 -	10/2010	10(O)	0/0
89	RESIDUE UPGRADEATION AND MS/HSD QUALITY IMPROVEMENT - [N16000021]IOCL,Gujarat	01/2007	5,693.00 6,898.00	6,898.00	5,735.33	01/2010 06/2010	11/2010	5(R3)	0/0
90	MSQ UPGRADEATION PROJECT AT DIGBOI REFINERY - [N16000037]IOCL,Assam	04/2008	356.00 -	300.00	212.91	02/2010 -	11/2010	9(O)	0/0
91	MSQ UPGRADEATION PROJECT AT BARAUNI REFINERY - [N16000038]IOCL,Bihar	04/2008	1,492.00 -	1,505.24	1,069.91	04/2010 -	11/2010	7(O)	0/0
92	SULTANPUR NEEMRANA PIPE LINE PROJECT (Spurline to CJPL) - [N16000049]GAIL,Multi State	11/2007	396.13 -	396.13	185.56	10/2009 06/2010	11/2010	5(R3)	0/0
93	INSTALLATION OF FCCV AT MUMBAI REFINERY - [N16000056]HPCL,Maharashtra	03/2007	900.47 -	900.47	679.84	09/2009 -	11/2010	14(O)	0/0
94	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON - [N16000009]BRPL,Assam	06/2006	1,431.91 1,646.39	1,676.00	1,438.72	09/2009 -	12/2010	15(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
95	Guru Govind Singh Refinery Products Evacuation Project - [N16000076]HPCL,Punjab	01/2009	605.40	605.40	282.40	12/2010	12/2010	0(O)	12/17
96	REFRIGERATED LPG STORAGE AT JNPT - [N16000083]BPCL,Maharashtra	06/2008	304.40	304.40	151.72	12/2010	12/2010	0(O)	0/0
97	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli - [N16000102]HPCL,Bihar	06/2009	613.54	727.88	315.52	12/2010	12/2010	0(O)	0/0
98	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00	224.00	132.52	12/2010 02/2011	02/2011	0(R3)	0/0
99	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10	600.00	542.47	03/2007	03/2011	48(O)	3/3
100	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 834.90	1,200.00	1,125.49	03/2007 03/2011	03/2011	0(R3)	6/6
101	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90	219.22	183.10	03/2006	03/2011	60(O)	6/6
102	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16	2,800.00	2,520.63	12/2008 12/2008	03/2011	27(R3)	0/0
103	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT - [N16000024]ONGC,Maharashtra	09/2006	2,305.30	2,305.30	2,061.15	06/2010 06/2010	03/2011	9(R3)	0/0
104	NORTH TAPTI GAS FIELD DEV. - [N16000085]ONGC,Gujarat	07/2008	589.70	755.76	20.84	03/2011	03/2011	0(O)	0/0
105	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	01/2010	589.70 755.56	755.56	20.84	03/2011	03/2011	0(O)	0/0
106	BAWANA NANGAL PIPE LINE PROJECT - [N16000050]GAIL,	07/2011	1,816.07 1,816.07	1,816.07	349.25	- 04/2011	04/2011	0(R3)	0/1
107	DAHEJ-VIJAYPUR PIPE LINE PROJECT(PHASE-II) - [N16000052]GAIL,Multi State	11/2007	4,429.38 4,403.00	2,800.00	1,697.61	10/2011 04/2011	04/2011	0(R3)	0/2
108	COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I - [N16000053]GAIL,Multi State	11/2007	1,512.00 1,434.00	1,434.00	644.05	04/2011 04/2011	04/2011	0(R3)	0/2
109	COMPRESSOR STATIONS (KAILARAS & CHAINSA) - [N16000054]GAIL,Multi State	11/2007	1,061.93 1,167.00	1,167.00	26.77	04/2011 04/2011	04/2011	0(R3)	0/2
110	HEERA RECONSTRUCTION - [N16000062]ONGC,Maharashtra	05/2008	706.70	706.70	456.65	04/2010	04/2011	12(O)	0/0
111	NEELAM RECONSTRUCTION - [N16000063]ONGC,Maharashtra	05/2008	305.08	305.08	84.89	04/2011	04/2011	0(O)	0/0
112	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,218.01	2,218.01	1,234.69	03/2005 05/2011	05/2011	0(R3)	0/0
113	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra	05/2008	333.40	330.40	0.39	05/2010	05/2011	12(O)	0/0
114	MNW-NF BRIDGE PROJECT - [N16000045]ONGC,Maharashtra	05/2008	175.21	162.12	-	03/2009	05/2011	26(O)	0/0
115	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32	463.32	-	06/2011	06/2011	0(O)	3/9

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
116	BNPL SPURLINE (UTTRANCHAL & PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92 -	540.92	0.95	06/2011 -	06/2011	0(O)	7/9
117	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 -	3,597.00	146.54	09/2011 -	09/2011	0(O)	0/0
118	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 -	3,284.00	109.26	09/2011 -	09/2011	0(O)	0/0
119	RESITMENT OF MARKETING INSTALATION AT VISAKH - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 -	756.00	468.73	12/2011 -	12/2011	0(O)	0/0
120	BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]IOCL,Gujarat	02/2009	349.00 -	349.00	114.41	08/2011 -	12/2011	4(O)	0/0
121	HYDROCRACKER REVAMP & SETTING - [N16000081]BPCL,	02/2008	825.00 -	825.00	78.49	- -	12/2011	-	0/203
122	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	154.37	12/2011 -	12/2011	0(O)	0/0
123	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 -	2,163.64	110.39	12/2011 -	12/2011	0(O)	0/0
124	Additional Development of D-1 Field - [N16000097]ONGC,Multi State	01/2010	2,163.64 -	2,163.64	110.39	12/2011 -	12/2011	0(O)	0/0
125	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	411.41	03/2010 03/2012	03/2012	0(R1)	0/0
126	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	6,652.22	-	01/2013 -	03/2012	-10(O)	0/0
127	DHABOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State	06/2009	4,543.43 4,508.38	4,508.38	10.46	03/2012 -	03/2012	0(O)	11/10
128	Integrated offshore crude Oil handling facilities at Paradip - [N16000090]IOCL,Maharashtra	12/2009	1,492.33 -	1,492.33	22.57	06/2012 -	03/2012	-3(O)	0/0
129	Assam gas Cracker project - [N16000106]BCPL,	04/2006	5,460.61 -	5,460.61	-	- -	04/2012	-	0/2
130	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 -	6,326.40	1,269.57	05/2010 -	05/2012	24(O)	0/0
131	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	1,552.63 2,920.82	2,920.82	164.51	02/2009 09/2010	05/2012	20(R1)	0/0
132	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 -	1,436.21	-	07/2010 -	05/2012	22(O)	0/0
133	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	45.51	03/2010 08/2010	06/2012	22(R1)	0/0
134	ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11 -	370.11	8.53	04/2011 -	07/2012	15(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
135	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC, Tripura	07/2008	288.04 288.04	288.04	-	08/2012 -	08/2012	0(O)	0/0
136	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC, Maharashtra	01/2009	6,855.93 -	6,855.93	931.54	09/2012 -	09/2012	0(O)	0/0
137	Paradip-Raipur-Sambalpur Ranchi Pipeline - [N16000088]IOCL, Maharashtra	08/2009	1,793.00 -	1,793.00	16.31	09/2012 -	09/2012	0(O)	0/0
138	Construction of six Effluent Treatment Plants (ETP) - [N16000099]ONGC, Gujarat	03/2009	234.78 234.78	234.78	-	09/2012 -	09/2012	0(O)	0/0
139	PARADIP REFINERY PROJECT - [N16000058]IOCL,	02/2009	29,777.00 -	29,777.00	4,256.49	- -	11/2012	-	0/103
140	KOCHI-KANJIRKOD BANGALORE-MANGALORE PIPELINE PROJECT PHASE-I - [N16000071]GAIL, Multi State	06/2009	3,032.00 348.00	348.00	7.27	03/2012 -	12/2012	9(O)	6/12
141	De-bottlenecking of SMPL - [N16000089]IOCL, Maharashtra	12/2009	1,584.00 -	1,584.00	1.55	- -	12/2012	-	0/0
142	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC, Maharashtra	10/2008	1,797.35 -	1,797.35	9.78	12/2011 -	01/2013	13(O)	0/0
143	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL, Uttar Pradesh	07/2010	1,000.00 -	1,000.00	7.93	01/2013 -	01/2013	0(O)	0/0
144	Butadiene Extraction Unit(BDEU) at Panipat - [N16000108]IOCL, Haryana	11/2009	341.50 -	342.00	-	02/2013 -	02/2013	0(O)	0/0
145	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC, Maharashtra	06/2007	1,252.75 8,813.41	8,813.41	5,208.06	06/2009 03/2013	03/2013	0(R3)	0/0
146	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, Assam	03/2009	2,465.15 -	2,378.86	211.94	03/2013 -	03/2013	0(O)	0/0
147	Construction of one Multipurpose Support Vessel - [N16000103]ONGC, Multi State	01/2010	723.64 -	723.64	-	03/2013 -	03/2013	0(O)	0/0
148	Development of Cluster-7 Fields - [N16000104]ONGC, Multi State	03/2010	3,241.03 -	3,241.03	-	03/2013 -	03/2013	0(O)	0/0
149	Development of WO-16 Cluster Fields - [N16000105]ONGC, Multi State	06/2010	2,523.00 -	2,523.00	-	01/2014 -	01/2014	0(O)	0/0
150	Wax Project - [N16000101]NRL, Assam	08/2010	576.60 -	576.60	6.48	02/2014 -	02/2014	0(O)	0/0
Total			144,690.62 -	160,094.89	45,689.10				113/491
Power									
151	National Capital Thermal Power Project Stage-II - [N18000013]NTPC, Uttar Pradesh	10/2006	5,135.33 -	5,135.33	-	10/2010 -	10/2010	0(O)	12/40
152	NORTHERN REGION SYSTEM STRENGTHENING-XI - [N18000034]PGCIL, Multi State	12/2007	417.76 -	417.76	262.75	12/2010 -	10/2010	-2(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
153	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-X - [N18000036]PGCIL,Uttar Pradesh	12/2007	408.36 -	408.36	298.06	12/2010 -	10/2010	-2(O)	0/0
154	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XII - [N18000039]PGCIL,Haryana	02/2008	261.55 -	261.55	137.87	11/2010 -	10/2010	-1(O)	0/0
155	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-IX - [N18000055]PGCIL,Multi State	07/2008	525.14 -	525.14	346.90	07/2011 -	10/2010	-9(O)	0/0
156	KOTESWAR TRANSMISSION SYSTEM (PGCIL) - [180100256]PGCIL,Uttaranchal	06/2006	260.34 -	241.27	151.56	06/2008 -	11/2010	29(O)	8/20
157	KORBA STPP STAGE-III - [N18000011]NTPC,Madhya pradesh	08/2006	2,448.50 -	2,448.49	2,059.00	02/2010 -	11/2010	9(O)	5/24
158	EAST-WEST TRANSMISSION CORRIDOR STRENGTHNING SCHEME - [260100100]PGCIL,Multi State	06/2006	803.70 -	803.76	612.68	06/2009 -	12/2010	18(O)	1/20
159	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Uttar Pradesh	10/2006	975.96 -	894.26	616.13	10/2009 -	12/2010	14(O)	2/20
160	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]NHPC,Multi State	12/2007	227.52 -	227.52	115.88	06/2010 -	12/2010	6(O)	0/0
161	TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB G - [N18000037]PGCIL,Haryana	04/2008	290.49 -	299.08	301.86	04/2010 -	12/2010	8(O)	0/0
162	WESTERN REGION STRENGTHENING SCHEME-VI - [N18000038]PGCIL,Gujarat	02/2008	340.72 -	340.72	147.53	11/2010 -	12/2010	1(O)	0/0
163	EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER - [N18000040]NHPC,Himachal Pr.	09/2007	262.10 -	262.10	138.79	09/2010 -	12/2010	3(O)	0/0
164	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37 -	297.37	210.33	07/2011 -	12/2010	-7(O)	0/0
165	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J & K	08/2005	1,729.29 -	1,724.79	1,211.77	11/2009 -	02/2011	15(O)	0/0
166	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J & K	08/2006	621.26 -	621.28	499.50	02/2011 -	02/2011	0(O)	0/1
167	Farakka STPP Stage-III - [N18000016]NTPC,West Bengal	07/2006	2,570.44 -	2,570.44	1,766.00	08/2010 -	02/2011	6(O)	13/26
168	WESTERN REGION STRENGTHENING SCHEME-IX - [N18000050]PGCIL,Multi State	04/2008	230.89 -	230.89	41.57	01/2011 -	02/2011	1(O)	0/0
169	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) - [180100260]PGCIL,Bihar	12/2005	3,779.46 -	3,725.13	3,409.04	09/2009 -	03/2011	18(O)	15/30
170	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23 -	4,978.56	2,585.00	07/2010 -	03/2011	8(O)	3/20

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
171	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69	477.69	313.87	09/2010	03/2011	6(O)	0/0
172	URI-II - [N18000023]PGCIL,J & K	10/2006	238.25	227.03	190.48	-	05/2011	-	0/0
173	SIMHADRI STPP STAGE -II (NTPC) - [N18000032]NTPC,Andhra Pradesh	08/2007	5,103.39	5,038.53	3,284.00	05/2011	05/2011	0(O)	0/0
174	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.56	2,304.52	1,123.71	10/2010	06/2011	8(O)	0/0
175	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HE - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24	639.52	377.38	01/2010	06/2011	17(O)	0/22
176	TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III - [N18000043]PGCIL,Multi State	12/2008	204.07	204.07	80.50	06/2011	06/2011	0(O)	0/0
177	TR. SYSTEM ASSOCIATED WITH CORBA III GENERATION PR - [N18000059]PGCIL,Madhya pradesh	02/2009	276.61	276.61	148.02	06/2011	06/2011	0(O)	0/0
178	NIMOO BAZGO HYDROELECTRIC PROJECT (NHPC) - [N18000006]NHPC,J & K	08/2006	611.01	611.02	512.92	08/2010	07/2011	11(O)	0/0
179	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10	196.10	21.55	07/2011	07/2011	0(O)	0/0
180	CHAMERA,STAGE-III (NHPC) - [180100241]NHPC,Himachal Pr.	08/2005	1,405.63	1,405.63	1,285.03	08/2010	08/2011	12(O)	0/0
181	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]PGCIL,Rajasthan	02/2009	210.79	210.79	92.36	08/2011	08/2011	0(O)	0/0
182	SYSTEM STRENGTHENING IN NR GRID FOR KARCHAM WANGTO - [N18000044]PGCIL,Multi State	12/2008	328.97	328.97	152.18	09/2011	09/2011	0(O)	0/0
183	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48	520.48	191.20	11/2011	11/2011	0(O)	0/0
184	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66	509.66	107.65	11/2011	11/2011	0(O)	0/0
185	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69	317.69	14.59	11/2011	11/2011	0(O)	0/0
186	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19	184.19	59.24	11/2011	11/2011	0(O)	0/0
187	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pr.	10/2002	4,527.15	4,527.15	3,315.00	04/2009	12/2011	32(O)	19/41
188	SIPAT STPP STAGE - I (NTPC) - [180100229]NTPC,Chhatisgarh	12/2003	8,323.39	8,323.39	6,993.00	12/2009	12/2011	24(O)	33/56
189	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01	623.44	57.71	01/2012	01/2012	0(O)	0/0
190	WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]PGCIL,Multi State	02/2009	664.96	664.96	66.55	02/2012	02/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
191	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]PGCIL,Multi State	02/2009	409.50	409.50	11.69	02/2012	02/2012	0(O)	0/0
192	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29	410.29	93.04	02/2012	02/2012	0(O)	0/0
193	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]PGCIL,Multi State	02/2009	353.57	353.57	139.59	07/2010	02/2012	19(O)	0/0
194	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32	1,347.32	436.80	02/2012	02/2012	0(O)	0/0
195	KOTESHWAR HEP(THDC) - [180100184]THDCL,Uttaranchal	04/2000	1,301.56	2,398.39	2,001.82	04/2005	03/2012	83(O)	2/22
196	KUNADANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29	2,159.07	1,608.50	11/2008	03/2012	40(O)	25/38
197	BONGAIGAON THERMAL POWER PROJECT (NTPC) - [N18000041]NTPC,Assam	01/2008	4,375.35	4,375.35	1,422.00	07/2011	03/2012	8(O)	0/0
198	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61	276.61	15.69	04/2012	04/2012	0(O)	0/0
199	765KV System for central part of Northern Region Grid - [N18000079]PGCIL,Multi State	11/2009	1,075.12	1,075.12	88.84	05/2012	05/2012	0(O)	0/0
200	765KV System for Central part of Northern Region G - [N18000078]PGCIL,Multi State	07/2009	1,736.36	1,736.36	-	06/2012	06/2012	0(O)	0/0
201	Immsdiate evacuation system for NABINAGAR TPS - [N18000082]PGCIL,Bihar	02/2010	215.86	215.86	24.68	06/2012	06/2012	0(O)	0/0
202	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34	232.34	4.65	06/2012	06/2012	0(O)	0/0
203	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38	1,061.38	799.39	09/2009	08/2012	35(O)	0/0
204	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pr.	12/2008	573.99	573.99	108.37	08/2012	08/2012	0(O)	4/9
205	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95	2,360.95	1,260.40	08/2012	08/2012	0(O)	0/0
206	765 KV POOLING STATION & NETWORK WITH DVC AND MAIT - [N18000069]PGCIL,Multi State	08/2008	7,075.33	7,075.33	2,433.20	08/2012	08/2012	0(O)	0/0
207	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83	1,216.83	99.04	08/2012	08/2012	0(O)	0/0
208	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2007	5,459.28	6,010.89	1,431.00	02/2012 08/2012	10/2012	2(R3)	0/0
209	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER - [N18000061]PGCIL,Multi State	10/2008	4,824.12	4,824.12	800.41	10/2012	10/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
210	MAUDA Transmission System - [N18000084]PGCIL,Maharashtra	02/2010	469.38	469.38	9.84	10/2012	10/2012	0(O)	0/0
211	Transmission System of Vindhuachal -IV & Rihand -I - [N18000076]PGCIL,Multi State	03/2010	4,672.99	4,672.99	11.89	11/2012	11/2012	0(O)	0/0
212	Northern Region Transmission Strengthening Scheme - [N18000083]PGCIL,Multi State	03/2012	965.58	965.58	69.52	11/2012	11/2012	0(O)	0/0
213	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI = II HEP - [180100261]PGCIL,Himachal Pr.	12/2005	358.42	358.42	6.57	12/2008 09/2010	12/2012	27(R1)	0/15
214	LOHARINAG-PAL HEP(4X150MW) - [N18000005]NTPC,Uttaranchal	06/2006	2,895.10	2,895.10	552.33	11/2011	12/2012	13(O)	6/34
215	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88	7,031.88	1,277.30	12/2012	12/2012	0(O)	0/0
216	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00	5,915.00	1,019.00	11/2012	12/2012	1(O)	0/0
217	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81	6,230.81	873.00	11/2012	12/2012	1(O)	0/0
218	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00	2,144.00	69.78	12/2012	12/2012	0(O)	0/0
219	Transmission System for phase-1 generation project - [N18000087]PGCIL,Orissa	09/2010	2,074.86	2,074.86	-	02/2013	02/2013	0(O)	0/0
220	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pr.	09/2002	3,919.59	3,919.59	2,903.19	09/2009	03/2013	42(O)	1/20
221	Tapovan-Vishnugad HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttaranchal	11/2006	2,978.48	2,978.48	912.00	03/2013	03/2013	0(O)	5/31
222	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pr.	12/2004	2,496.90	2,496.90	1,229.44	05/2013 05/2013	05/2013	0(R3)	77/49
223	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19	11,130.19	1,353.80	08/2013	08/2013	0(O)	0/0
224	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pr.	01/2007	2,047.03	2,047.03	952.75	01/2012	09/2013	20(O)	2/10
225	BARH STTP STAGE -II (NTPC) - [N18000047]NTPC,Bihar	02/2008	7,341.04	7,341.04	1,105.00	08/2013	10/2013	2(O)	0/0
226	LOWER SUBANSIRI H.E.P (NHPC) - [180100221]NHPC,Arunachal Pr.	09/2003	6,285.33	7,451.99	4,181.57	09/2010	12/2013	39(O)	2/11
227	BARH STTP(3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97	8,692.97	5,057.00	11/2010	09/2014	46(O)	15/51
228	Transm System for development of Pooling stn. in N - [N18000077]PGCIL,West Bengal	04/2010	4,404.57	4,404.57	-	01/2015	01/2015	0(O)	0/0
229	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttaranchal	07/2006	1,657.00	3,124.76	249.07	07/2010	03/2015	56(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
230	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttaranchal	08/2008	2,491.58	2,491.58	122.73	07/2014	03/2015	8(O)	0/8
231	KISHANGANGA HEP - [N18000031]NHPC,J & K	07/2007	2,238.67	3,642.04	472.88	07/2014	01/2016	18(O)	0/0
232	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,Manipur	12/1999	578.62	578.62	28.33	06/2006	-	-	0/0
233	TUIRIAL HE PROJECT(NEEPCO) - [180100165]NEEPCO,Mizoram	07/1998	368.72	913.63	216.79	07/2006	-	-	2/5
234	SEWA- II H.E.P (NHPC) - [180100220]NHPC,J & K	09/2003	665.46	1,016.74	961.39	09/2007	-	-	8/36
235	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45	947.96	773.55	12/2007	-	-	14/18
	Total		180,925.92	188,054.62	70,486.99				274/677
Health & Family Welfare									
236	NORTH EAST INDIRA GANDHI INSTITUTE OF HEALTH & MS - [210100001]H&FW,Meghalaya	05/1986	71.18	443.15	547.78	03/1999	-	-	7/16
	Total		71.18	443.15	547.78				7/16
Railways									
237	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34	296.20	265.87	04/2003	06/2010	3(R1)	0/0
238	VALLAPARPADM-IDAPALLY,(NL)(RVNL) - [N22000048]RVNL,Kerala	07/2006	246.50	246.50	323.67	03/2009	11/2009	8(R3)	0/0
239	DHARMAVARAM-PAKALA (GC), SCR - [220100282]SCR,Andhra Pradesh	04/1997	200.00	610.07	567.49	-	03/2010	13(R1)	0/0
240	BHILDI-SAMDARI (GC) - [220100291]RVNL,Gujarat	04/1999	244.74	479.00	476.85	-	03/2010	12(R1)	0/0
241	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00	732.80	228.70	03/2008	03/2010	21(R3)	0/0
242	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94	325.00	304.76	-	09/2010	-	0/0
243	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322]WR,Gujarat	04/2005	148.61	227.52	241.13	03/2008	10/2010	19(R1)	0/0
244	DEOGHAR-DUMKA NEW BG LINE (DOUBL.)(ER) - [220100264]ER,Jharkhand	02/1999	180.73	358.00	322.19	12/2006	11/2010	23(R1)	0/0
245	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23	638.00	-	02/2015	11/2010	-51(O)	0/0
246	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MTP,Maharashtra	03/1996	401.81	495.44	155.05	03/2004	12/2010	81(O)	0/0
247	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Multi State	09/2001	100.00	724.31	691.36	-	12/2010	-	0/0
248	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16	243.40	205.78	-	12/2010	22(R1)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
249	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	211.90	155.49	- 03/2009	12/2010	21(R1)	0/0
250	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	221.90	124.14	12/2007 03/2010	12/2010	9(R1)	0/0
251	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL,Uttar Pradesh	04/2003	230.73 399.73	399.50	267.19	03/2009 12/2008	12/2010	24(R1)	0/0
252	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN - [N22000081]RVNL,Gujarat	09/2005	200.80 200.80	200.80	173.77	- -	12/2010	-	0/0
253	MUMBAI URBAN TRANSPORT PROJECT PHASE-I, MTP - [N22000093]MRTP,Maharashtra	04/2003	3,125.20 -	4,103.20	3,866.40	- -	12/2010	-	0/1
254	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]ECR,Bihar	03/1997	100.00 -	322.29	367.27	- -	02/2011	-	0/0
255	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	475.16	405.65	02/2010 -	02/2011	12(O)	0/0
256	SHIMOGA-TALAGUPPA (SWR), GC - [N22000056]GC,Karnataka	12/1992	46.00 -	405.60	223.83	- -	02/2011	-	0/0
257	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 -	356.87	127.41	- 03/2010	03/2011	12(R1)	0/0
258	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 175.30	488.76	355.55	06/1999 -	03/2011	141(O)	0/0
259	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhandd	04/1997	193.78 -	456.45	247.29	06/2004 -	03/2011	81(O)	0/0
260	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	925.00	472.80	05/2008 -	03/2011	34(O)	0/0
261	AGRA-ETAWAH VIA FATEBAD & BAD (NL),NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 -	214.09	152.40	12/2009 -	03/2011	15(O)	0/0
262	GOOTY- RENIGUNTA PATCH DOUBLING PH-II (DL) (SCR) - [220100267]SCR,Andhra Pradesh	05/2002	304.50 -	306.00	341.81	- -	03/2011	-	0/0
263	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECR,Orissa	04/1994	355.38 -	700.00	102.44	- -	03/2011	-	0/0
264	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd	04/1996	371.36 -	452.35	266.35	- -	03/2011	-	0/0
265	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/1997	143.92 -	168.80	70.43	- -	03/2011	-	0/0
266	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	200.73 -	230.03	129.96	- -	03/2011	-	0/0
267	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	273.00	263.77	- 03/2009	03/2011	24(R1)	0/0
268	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 283.95	348.78	317.20	- -	03/2011	-	0/0
269	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 329.70	329.70	268.75	03/2009 12/2009	03/2011	15(R1)	0/0
270	ALUABARI ROAD SILIGURI JANCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 255.96	272.11	212.76	- -	03/2011	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
271	BARDHAMAN-KATWA, ER (GC) - [N22000091]GC, West Bengal	04/2007	245.15	245.15	59.41	12/2010	03/2011	3(O)	0/0
272	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE, Uttar Pradesh	02/2008	171.10	171.10	43.83	03/2011	03/2011	0(O)	0/0
273	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE, Uttar Pradesh	03/2006	258.35	258.35	9.38	03/2011	03/2011	0(O)	0/0
274	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]GC, Gujarat	04/2006	196.97	196.97	121.12	03/2011	03/2011	0(O)	0/0
275	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL, West Bengal	09/2007	252.50	252.50	93.70	02/2010	11/2011	21(O)	0/0
276	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, Orissa	04/1996	301.64	735.10	-	-	12/2011	27(R1)	0/0
277	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]ECR, Bihar	04/1997	233.00	727.52	474.43	09/2009	03/2012	-	0/0
278	KOSI BRIDGE (NL), ECR - [220100304]ECR, Bihar	04/2002	323.41	341.41	182.22	-	03/2012	-	0/0
279	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECR, Orissa	04/2005	726.96	810.78	75.92	-	03/2012	-	0/0
280	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP, Tamil Nadu	04/2006	415.59	495.74	83.95	-	03/2012	-	0/0
281	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL, Chhatisgarh	09/2006	324.90	324.90	116.94	03/2010	03/2012	24(O)	0/0
282	TAMLUK DIGHA - [N22000097]LD, West Bengal	03/1984	293.97	293.97	313.13	06/2005	04/2012	82(O)	0/0
283	NANGALDAM-TALWARA(NL), NR - [220100188](NR), Multi State	03/1981	37.68	730.00	284.98	-	07/2012	-	0/0
284	GUNA-ETAWAH(NCR), NL - [220100007]NCR, Multi State	04/1985	158.77	540.96	479.30	03/1994	12/2012	225(O)	0/0
285	CONV.OF 1500V DC TRACTION TO 25 KV AC, WR - [220100233]RE, Maharashtra	07/1996	273.67	1,800.00	501.49	-	12/2012	-	0/0
286	CHANDIGARH-LUDHIANA(NEW BG LINE), NR - [220100241](NR), Punjab	07/1997	248.44	1,103.47	679.18	-	12/2012	-	0/0
287	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER, Uttar Pradesh	03/2002	383.15	863.23	325.79	-	12/2012	-	0/0
288	JIND-SONEPAT (NL), NR - [220100280](NR), Haryana	01/2004	190.81	234.45	158.56	-	12/2012	-	0/0
289	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR, Bihar	04/2002	921.00	981.00	340.69	03/2009	12/2012	45(O)	0/0
290	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR, Bihar	04/2001	624.47	1,480.71	445.84	10/2007	12/2012	62(O)	0/0
291	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, Madhya pradesh	09/2007	687.20	687.20	125.24	03/2010	12/2012	33(O)	0/0
292	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]LD, Uttar Pradesh	04/2006	325.00	369.90	88.21	03/2010	12/2012	33(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
293	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84	410.08	101.53	-	03/2013	-	0/0
294	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00	1,029.00	597.31	-	03/2013	-	0/0
295	RANGIA-MURKONGSELEK, (GC) NEFR - [220100315]NEFR,Multi State	01/2004	912.70	1,556.23	295.30	-	03/2013	-	0/0
296	BRAHAMAPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	04/1996	1,000.00	3,230.02	1,920.25	04/2008 12/2011	03/2014	27(R1)	0/0
297	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	02/2000	733.00	1,655.80	520.84	12/2008	03/2014	63(O)	0/0
298	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00	160.48	98.53	-	03/2014	-	0/0
299	NEW B.G. LINE FROM AZARA TO BYRNIHAT (NATIONAL PRO - [N22000086]NEFR,Assam	09/2006	200.00	390.00	0.78	-	03/2014	-	0/0
300	AGARTALA SABROOM, NL, NEFR - [N22000099]NL,Tripura	04/2008	813.34	813.34	98.94	03/2014	03/2014	0(O)	0/0
301	BHAIRABI SAIRONG, NEFR - [N22000100]NL,Mizoram	04/2008	619.34	2,429.41	1.61	04/2014	03/2014	-1(O)	0/0
302	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66	324.66	134.14	-	03/2015	-	0/0
303	MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP - [N22000092]MRTP,Maharashtra	04/2008	5,300.00	5,300.00	128.02	03/2014	03/2015	12(O)	0/0
304	SEVOK RANGPO, NEFR - [N22000102]LD,Sikkim	04/2008	1,339.48	3,380.57	2.56	12/2015	12/2015	0(O)	0/0
305	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Multi State	04/2003	727.56	3,123.52	237.63	03/2011	03/2016	60(O)	0/0
306	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J & K	03/1995	2,500.00	11,270.00	6,481.16	03/2001	12/2017	201(O)	0/0
307	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00	634.13	556.48	03/1995	-	-	0/0
308	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43	617.63	378.63	-	-	-	0/0
309	RAJKOT-VERAVAL (GC) AND WANSJALIYA-JETALSAR GC AN - [220100116]WR,Gujarat	04/1992	112.53	464.50	501.12	03/1996 06/2009	-	-	0/0
310	HOTGI-GADAG(GC),SWR - [220100125]SWR,Multi State	04/1994	180.00	318.66	452.61	03/1999 03/2003	-	-	0/0
311	AMBALA-MORADABAD(RE) - [220100131]RE,Multi State	03/1993	152.21	265.00	265.33	03/1998	-	-	0/0
312	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	01/1986	36.80	285.93	232.05	-	-	-	0/0
313	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECR,Orissa	04/1993	100.00	170.00	135.03	03/2002 03/2011	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
314	DALLIRAJHARA-JAGDALPUR,NL,SECR - [220100149]SECR,Chhatisgarh	04/1995	369.00 -	968.60	0.43	- -	-	-	0/0
315	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	579.37	578.85	- -	-	-	0/0
316	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhandd	04/1995	184.00 -	675.00	353.44	- 12/2011	-	-	0/0
317	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 -	1,010.00	67.32	- -	-	-	0/0
318	AJMER-UDAIPUR-CHITTAURGARH (GC),NWR - [220100185]NWR,Rajasthan	09/1996	262.00 433.39	456.00	470.63	- 03/2000	-	-	0/0
319	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	356.00 -	511.86	413.02	03/1998 -	-	-	0/0
320	KADUR-CHIKMAGALUR-SAKLIESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 -	465.00	104.45	- -	-	-	0/0
321	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 -	712.00	399.69	- -	-	-	0/0
322	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1997	155.74 164.36	429.49	352.10	02/2009 -	-	-	0/0
323	HUBLI-AKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00 -	337.82	53.93	- -	-	-	0/0
324	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	1,548.95	1,101.82	- -	-	-	0/0
325	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1996	377.32 236.41	497.47	72.33	- -	-	-	0/0
326	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 154.30	154.30	106.79	03/2007 03/2007	-	-	0/0
327	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 -	363.26	0.27	07/2008 -	-	-	0/0
328	KODERMA-RANCHI VIA BARKAKHANA (NL),ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 -	1,099.20	711.79	07/2005 -	-	-	0/0
329	KUTTIPURAM-CALICUT INCLD. SHORANUR-M-LORE (DL) (SR) - [220100249]SR,Kerala	03/2001	178.76 177.34	219.94	190.49	- -	-	-	0/0
330	VILLUPURAM-KATPADI (GC)(SR) - [220100251]SR,Tamil Nadu	02/2000	175.00 -	513.16	500.57	- -	-	-	0/0
331	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	550.00	64.99	- -	-	-	0/0
332	PURNA-AKOLA (G.C), SCR - [220100253]SCR,Maharashtra	02/2000	228.00 -	497.63	477.14	- -	-	-	0/0
333	BIDAR-GULBARGA,SCR(NL) - [220100254]SCR,Karnataka	02/1999	242.42 369.70	369.70	159.67	- 05/2009	-	-	0/0
334	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	09/2001	320.10 -	522.56	282.57	- -	-	-	0/1
335	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	03/1997	78.23 -	162.87	79.22	- -	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
336	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 408.76	639.54	776.06	06/2007 -	-	-	0/0
337	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 -	548.96	418.89	- -	-	-	0/0
338	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 -	695.00	9.41	- -	-	-	0/0
339	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 -	228.09	159.82	- -	-	-	0/0
340	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 240.59	607.09	240.54	- 12/2012	-	-	0/0
341	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 -	1,300.00	0.29	- -	-	-	0/0
342	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 -	325.17	311.98	03/2005 12/2008	-	-	0/0
343	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91 -	418.17	52.53	- -	-	-	0/0
344	RAJGIR-TILAIYA (NL), ECR - [220100312]ECR,Bihar	04/2001	180.82 180.82	180.82	264.46	03/2006 -	-	-	0/0
345	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	1,225.00	148.10	- -	-	-	0/0
346	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	104.10 -	218.19	72.12	- -	-	-	0/0
347	KICHHA-KHATIMA (NL) - NER - [220100317]NER,Uttaranchal	04/2003	165.67 -	165.67	0.15	- -	-	-	0/0
348	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	102.78	- -	-	-	0/0
349	GUNTUR-GUNTAKAL-KALLURU(GL)(SCR) - [220100330]SCR,Andhra Pradesh	04/1992	458.45 -	573.12	555.49	- -	-	-	0/0
350	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 -	671.82	0.74	- -	-	-	0/0
351	GAELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhandd	03/1998	186.92 -	261.70	0.08	02/2006 -	-	-	0/0
352	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 -	224.51	41.39	- -	-	-	0/0
353	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 -	881.19	86.35	- -	-	-	0/0
354	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 -	900.00	72.83	- -	-	-	0/0
355	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 -	900.00	251.23	- -	-	-	0/0
356	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 -	227.40	15.35	- -	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
357	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 -	582.83	38.60	- -	-	-	0/0
358	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	529.88	26.09	- -	-	-	0/0
359	KISHANGANJ JALALGARH, NEFR - [N22000101]NL,Bihar	04/2008	282.92 -	333.76	0.71	- -	-	-	0/0
360	RESTORATION WITH GAUGE CONVERSION OF SILIGHAT TOWN - [N22000103]GC,Assam	04/1993	100.41 -	949.22	15.65	12/2009 -	-	-	0/0
361	MIRAJ-LATUR ROAD(GC),CR - [220100162]CR,Maharashtra	04/1993	225.00 323.00	816.40	816.00	03/2001 -	-	-	0/0
362	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	913.51	431.87	- -	-	-	0/0
363	SURENDRANAGAR-BHAVNAGAR(GC),WR - [220100187]WR,Gujarat	03/1997	437.40 -	563.25	540.37	03/2004 03/2010	-	-	0/0
364	TOLLYGANJ-GARIA with extension to Dum Dum-Naopara - [220100268]MRTP,West Bengal	03/2000	907.69 1,032.76	5,608.50	2,664.44	12/2006 08/2010	-	-	0/0
365	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 -	762.33	292.34	- 12/2009	12/2010	12(R1)	0/0
Total			49,023.84 -	104,193.13	45,786.84				0/2
Road Transport & Highways									
366	COCHIN PORT, NH-47 (PORT CONNECTIVITY) KMS 348 - KMS 358 - [240100206]NHAI,Kerala	04/2000	106.00 -	193.00	141.70	08/2006 -	10/2010	50(O)	0/0
367	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2 - [240106222]NHAI,Uttar Pradesh	12/2003	193.00 -	193.00	284.10	10/2008 -	10/2010	24(O)	0/0
368	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28 - [240106225]NHAI,Uttar Pradesh	12/2003	217.00 -	217.00	310.30	10/2008 -	10/2010	24(O)	0/0
369	GORAKHPUR-AYODHYA (LMNHP-6),NH-28, KM.251.70 TO KM.208.00 - [240106245]NHAI,Uttar Pradesh	12/2003	239.00 -	239.00	389.90	10/2008 -	10/2010	24(O)	0/0
370	JALANDAR-AMRITSAR, KM.407/100 TO KM.456/100, NH-1 - [240106268]NHAI,Punjab	03/2005	263.00 -	263.00	420.80	02/2009 -	10/2010	20(O)	0/0
371	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 251-293 - [N24000076]NHAI,Andhra Pradesh	12/2003	208.46 -	208.46	193.70	08/2009 -	10/2010	14(O)	0/0
372	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 293.4-3 - [N24000077]NHAI,Andhra Pradesh	12/2003	239.19 -	239.19	224.50	09/2009 -	10/2010	13(O)	0/0
373	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 336-376 - [N24000078]NHAI,Andhra Pradesh	12/2003	243.38 -	243.38	261.40	09/2008 -	10/2010	25(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
374	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 376-418 - [N24000079]NHAI,Andhra Pradesh	12/2003	205.92	205.92	204.40	08/2009	10/2010	14(O)	0/0
375	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 418-463 - [N24000080]NHAI,Andhra Pradesh	12/2003	243.64	243.64	254.70	08/2009	10/2010	14(O)	0/0
376	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 211-251 - [N24000081]NHAI,Andhra Pradesh	12/2003	194.80	194.80	174.00	08/2009	10/2010	14(O)	0/0
377	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI, Madhya pradesh	12/2003	263.17	263.17	232.50	09/2009	10/2010	13(O)	0/0
378	BANGALORE-NEELAMANGLALA NH-4 - [N24000104]NHAI,Karnataka	03/2005	445.00	445.00	802.00	07/2010	10/2010	3(O)	0/0
379	BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4 - [N24000106]NHAI,Karnataka	03/2005	565.00	565.00	881.00	07/2010	10/2010	3(O)	0/0
380	AMRITSAR-WAGHA BORDER - [N24000121]NHAI,Punjab	06/2008	205.88	205.88	214.90	06/2010	10/2010	4(O)	0/0
381	CHENNAI BYPASS (NHAI) OTHERS, NH-45, 4 & 5 - [240106202]NHAI,Tamil Nadu	12/2003	480.00	480.00	837.90	11/2007	11/2010	36(O)	0/0
382	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B - [240106276]NHAI,Tamil Nadu	03/2005	629.00	629.00	876.90	11/2010	11/2010	0(O)	0/0
383	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00	196.65	99.15	08/2004	12/2010	76(O)	0/0
384	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00	207.56	110.72	08/2004	12/2010	76(O)	0/0
385	PURNEA-GOYAKOTA SEC.(EW) (NS & EW-PH-I) KM.419-KM.447, NH-31 - [240103191]NHAI,Bihar	04/2000	205.73	205.73	244.30	07/2004	12/2010	77(O)	0/0
386	IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS - [240106203]NHAI,Tamil Nadu	12/2003	210.00	210.00	653.80	04/2007	12/2010	44(O)	0/0
387	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI,Uttar Pradesh	12/2003	275.00	275.00	284.00	09/2007	12/2010	39(O)	0/0
388	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]NHAI,Gujarat	12/2003	412.78	479.54	424.60	11/2007	12/2010	37(O)	0/0
389	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI,J & K	12/2003	193.09	193.09	140.30	03/2008	12/2010	33(O)	0/0
390	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J & K	12/2003	166.27	166.27	105.30	03/2008	12/2010	33(O)	0/0
391	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]NHAI,Punjab	12/2003	284.00	284.00	299.10	05/2008	12/2010	31(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
392	MADURAI -KANIAKUMARI SECTION (NS-41/TN) NH-7,KM.80 TO KM.120 - [240106240]NHAI,Tamil Nadu	12/2003	323.36 -	323.36	189.90	03/2008 -	12/2010	33(O)	0/0
393	GORAKHPUR-AYODHYA (LMNHP-4),NH-28, KM.164.00 TO KM.135.00 - [240106247]NHAI,Uttar Pradesh	12/2003	205.00 -	205.00	312.40	10/2008 -	12/2010	26(O)	0/0
394	AYODHYA-LUCKNOW (LMNHP-3),NH-28, KM.135.000 TO KM.93.075 - [240106248]NHAI,Uttar Pradesh	12/2003	212.00 -	212.00	330.60	10/2008 -	12/2010	26(O)	0/0
395	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00 -	190.00	221.70	01/2009 -	12/2010	23(O)	0/0
396	NAGAON BYPASS (NH-37)(NHAI) - [240106289]NHAI,Assam	12/2003	230.00 -	230.00	289.00	06/2008 -	12/2010	30(O)	0/0
397	DARBHANGA-MUZAFFARPUR(KM 30 TO KM 0), NH-57 (NHAI) - [240106296]NHAI,Bihar	12/2003	291.80 -	291.80	425.50	06/2008 -	12/2010	30(O)	0/0
398	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	250.39	253.20	10/2008 -	12/2010	26(O)	0/0
399	SAGAR - RAJMARG CHORAHA,KM 255-297, NH-26 (NHAI) - [240106302]NHAI,Madhya pradesh	12/2003	206.96 -	206.96	281.90	10/2008 -	12/2010	26(O)	0/0
400	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	225.00	169.80	07/2008 -	12/2010	29(O)	0/0
401	THRISSUR TO ANGAMALI (NH-47) - [N24000037]NHAI,Kerala	12/2003	312.50 -	312.50	477.00	03/2009 -	12/2010	21(O)	0/0
402	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50 -	196.50	196.10	06/2008 -	12/2010	30(O)	0/0
403	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82 -	221.82	186.30	11/2008 -	12/2010	25(O)	0/0
404	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00 -	168.00	305.42	12/2008 -	12/2010	24(O)	0/0
405	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	280.00	573.00	06/2009 -	12/2010	18(O)	0/0
406	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60 -	407.60	182.00	06/2010 -	12/2010	6(O)	0/0
407	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70 -	228.70	88.78	02/2004 -	12/2010	82(O)	0/0
408	GONDE-VADAPE(THANE), NH-3, KM.440/000 TO KM.539/500 - [240106262]NHAI,Maharashtra	03/2005	579.00 -	579.00	678.70	04/2009 -	01/2011	21(O)	0/0
409	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00 -	200.00	186.80	06/2008 -	01/2011	31(O)	0/0
410	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93 -	300.93	232.10	10/2009 -	01/2011	15(O)	0/0
411	TRICHY - DINDIGUAL NH-45 - [N24000099]NHAI,Tamil Nadu	03/2005	576.00 -	576.00	340.00	07/2010 -	01/2011	6(O)	0/0
412	PONDICHERY - TINDIVANAU NH-66 - [N24000100]NHAI,Tamil Nadu	03/2005	285.00 -	285.00	240.00	07/2010 -	01/2011	6(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
413	END OF DURG BYPASS- CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI, Chhatisgarh	01/2008	464.00 -	464.00	391.70	01/2011 -	01/2011	0(O)	0/0
414	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, Assam	12/2003	157.47 -	154.57	137.80	09/2007 -	03/2011	42(O)	0/0
415	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI, West Bengal	04/2000	273.00 -	522.00	333.40	03/2005 -	03/2011	72(O)	0/0
416	JHANSI BYPASS (UP-3), KM.104- KM.91, NH-25 - [240106220]NHAI, Uttar Pradesh	12/2003	158.06 -	158.06	157.80	08/2005 -	03/2011	67(O)	0/0
417	MEHSI TO KOTWA (LMNHP-II), PH.II, KM.480 TO KM.440, NH-28 - [240106223]NHAI, Bihar	12/2003	239.00 -	239.00	265.10	07/2005 -	03/2011	68(O)	0/0
418	MUZZAFFARPUR TO MEHSI (LMNHP- 12), KM.520 TO 480, NH-28 - [240106224]NHAI, Bihar	12/2003	275.00 -	275.00	292.40	07/2005 -	03/2011	68(O)	0/0
419	KOTWA TO DEWAPUR(10 LMNHP), NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI, Bihar	12/2003	240.00 -	240.00	202.50	10/2008 -	03/2011	29(O)	0/0
420	ORAI TO JHANSI (UP-4), NH-25, KM.170.0 TO KM.104.0 - [240106249]NHAI, Uttar Pradesh	12/2003	451.97 -	451.97	502.00	04/2008 -	03/2011	35(O)	0/0
421	ORAI TO JHANSI (UP-5), NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI, Uttar Pradesh	12/2003	340.68 -	340.68	300.70	03/2008 -	03/2011	36(O)	0/0
422	MEERUT-MUZZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00 - [240106256]NHAI, Uttar Pradesh	03/2005	359.00 -	359.00	570.30	03/2009 -	03/2011	24(O)	0/0
423	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, Assam	12/2003	280.00 -	280.00	139.40	02/2009 -	03/2011	25(O)	0/0
424	LANKA TO DABOKA (NH-54)(NHAI) - [240106286]NHAI, Assam	12/2003	225.00 -	225.00	201.60	06/2008 -	03/2011	33(O)	0/0
425	LALITPUR TO SAGAR, NH-26 (NHAI) - [240106299]NHAI, Madhya pradesh	12/2003	198.00 -	198.00	132.10	11/2008 -	03/2011	28(O)	0/0
426	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI, Madhya pradesh	12/2003	225.00 -	225.00	205.30	10/2008 -	03/2011	29(O)	0/0
427	RINGBUNDS TO JHAJHANPUR (BR-6) - [N24000030]NHAI, Bihar	12/2003	340.00 -	340.00	485.10	06/2008 -	03/2011	33(O)	0/0
428	SITAPUR-LUCKNOW - [N24000036]NHAI, Uttar Pradesh	03/2005	322.00 -	322.00	275.40	06/2009 -	03/2011	21(O)	0/0
429	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, Assam	12/2003	245.00 -	245.00	245.90	03/2008 -	03/2011	36(O)	0/0
430	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, Assam	12/2003	225.00 -	225.00	144.50	06/2008 -	03/2011	33(O)	0/0
431	BARA TO ORAI, NH-2, 25 - [N24000069]NHAI, Uttar Pradesh	12/2003	465.00 -	465.00	33.65	04/2009 -	03/2011	23(O)	0/0
432	KURALI-KIRATPUR, NH-21 - [N24000087]NHAI, Punjab	03/2005	309.00 -	309.00	485.20	06/2010 -	03/2011	9(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
433	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, Multi State	12/2003	604.00	604.00	257.40	12/2009	03/2011	15(O)	0/0
434	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI, Uttar Pradesh	12/2003	355.06	355.06	243.50	09/2009	03/2011	18(O)	0/0
435	JHANSI TO LALITPUR, NH-26 - [N24000097]NHAI, Uttar Pradesh	12/2003	276.09	276.09	184.60	09/2009	03/2011	18(O)	0/0
436	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI, Karnataka	03/2005	441.00	441.00	632.80	07/2010	03/2011	8(O)	0/0
437	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI, Multi State	12/2003	232.45	232.45	123.00	09/2010	03/2011	6(O)	0/0
438	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI, Uttar Pradesh	04/2000	367.49	367.49	453.68	03/2005	04/2011	73(O)	0/0
439	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, Assam	12/2003	200.00	200.00	63.10	04/2009	04/2011	24(O)	0/0
440	GANJAM-ICCHAPURUM, NH-5(NHAI) - [N24000057]NHAI, Orissa	04/2000	263.27	263.27	220.42	02/2004	04/2011	86(O)	0/0
441	KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]NHAI, Uttar Pradesh	12/2003	242.00	242.00	328.50	12/2008	05/2011	29(O)	0/0
442	ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) - [N24000117]NHAI, Multi State	02/2008	295.00	295.00	475.80	08/2010	05/2011	9(O)	0/0
443	KALGHAT-MP/MAHARASHTRA BORDER KM 16.6-84.70 - [N24000119]NHAI, Madhya pradesh	11/2008	549.00	549.00	641.80	05/2010	05/2011	12(O)	0/0
444	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, Haryana	04/2007	486.00	486.00	287.00	05/2010	05/2011	12(O)	0/0
445	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI, Uttar Pradesh	03/2005	220.00	220.00	168.80	09/2007	06/2011	45(O)	0/0
446	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, Uttar Pradesh	12/2003	155.00	201.66	61.17	09/2008	06/2011	33(O)	0/0
447	GORAKHPUR-AYODHYA (LMNHP-5), NH-28, KM.208.00 TO KM.164.00 - [240106246]NHAI, Uttar Pradesh	12/2003	227.00	227.00	-	10/2008	06/2011	32(O)	0/0
448	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI, Uttar Pradesh	12/2003	227.00	227.00	306.80	12/2008	06/2011	30(O)	0/0
449	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI, Bihar	12/2003	332.94	332.94	219.90	09/2008	06/2011	33(O)	0/0
450	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, Madhya pradesh	12/2003	251.03	251.03	205.60	10/2008	06/2011	32(O)	0/0
451	RAJMARG CHORAHA TO LAKHNANDON, KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI, Madhya pradesh	12/2003	229.91	229.91	150.30	10/2008	06/2011	32(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
452	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, Assam	12/2003	160.00	160.00	85.57	05/2008	06/2011	37(O)	0/0
453	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI, Uttar Pradesh	12/2003	600.24	600.24	524.20	10/2009	06/2011	20(O)	0/0
454	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]NHAI, Bihar	12/2003	418.04	418.04	252.70	03/2010	06/2011	15(O)	0/0
455	TRICHY - KORUR NH-67 - [N24000101]NHAI, Tamil Nadu	03/2005	516.00	516.00	452.20	07/2010	06/2011	11(O)	0/0
456	SALEM - U / UNDRUPET (BOT -1/TN-06) NH -68 - [N24000102]NHAI, Tamil Nadu	03/2005	941.00	941.00	598.50	01/2011	06/2011	5(O)	0/0
457	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI, Orissa	04/2000	225.00	225.00	-	04/2004	10/2011	90(O)	0/0
458	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI, Assam	12/2003	225.00	225.00	203.40	06/2008	10/2011	40(O)	0/0
459	NH CONNECTIVITY TO ICTT VALLARPADAUE NH - SH - [N24000107]NHAI, Kerala	03/2005	557.00	557.00	914.50	02/2010	10/2011	20(O)	0/0
460	DARBHANGA-MUZAFFARPUR, NH-57 (NHAI) - [240106295]NHAI, Bihar	12/2003	305.00	305.00	462.00	06/2008	11/2011	41(O)	0/0
461	SAGAR BY PASS, KM 187 TO KM 211, NH-26 (NHAI) - [240106301]NHAI, Uttar Pradesh	12/2003	151.30	151.30	130.00	10/2008	11/2011	37(O)	0/0
462	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI, Assam	12/2003	230.00	230.00	132.90	06/2005	12/2011	78(O)	0/0
463	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI, Assam	12/2003	195.00	195.00	125.40	06/2008	12/2011	42(O)	0/0
464	BIJNI TO ASSAM/WB BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI, Assam	12/2003	237.80	237.80	119.60	06/2008	12/2011	42(O)	0/0
465	SAGAR - RAJMARG CHORAH, KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI, Madhya Pradesh	12/2003	203.43	203.43	138.60	10/2008	12/2011	38(O)	0/0
466	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI, Bihar	12/2003	340.00	340.00	344.90	09/2008	12/2011	39(O)	0/0
467	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, Assam	12/2003	264.72	264.72	189.00	06/2008	12/2011	42(O)	0/0
468	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00	208.00	163.80	04/2008	12/2011	44(O)	0/0
469	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI, Assam	12/2003	200.00	200.00	150.20	06/2008	12/2011	42(O)	0/0
470	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, Assam	12/2003	175.96	175.96	95.16	04/2008	03/2012	47(O)	0/0
471	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, Assam	12/2003	198.16	198.16	137.80	04/2008	03/2012	47(O)	0/0
472	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, Rajasthan	12/2003	275.00	281.31	177.32	02/2010	03/2012	25(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
473	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, Maharashtra	03/2005	940.00	940.00	95.50	07/2012	07/2012	0(O)	0/0
474	PATHANKOT BHOGPUR NH-1A - [N24000115]NHAI, Punjab	12/2003	229.00	229.00	47.42	05/2010	08/2012	27(O)	0/0
475	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, Assam	12/2003	217.61	217.61	75.75	04/2010	12/2012	32(O)	0/0
476	AGRA-BYPASS(NS-1/UP-1), KM 176.8-13.03 NH-2,3 - [N24000098]NHAI, Uttar Pradesh	12/2003	348.16	348.16	108.90	09/2007	06/2013	69(O)	0/0
477	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, Assam	12/2003	199.81	199.81	28.39	04/2009	12/2013	56(O)	0/0
478	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, Assam	12/2003	167.64	167.64	39.49	11/2008	12/2013	61(O)	0/0
479	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, Assam	12/2003	155.04	155.04	28.27	11/2008	12/2013	61(O)	0/0
480	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI, Assam	12/2003	212.00	212.00	35.04	09/2007	12/2013	75(O)	0/0
481	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, Assam	12/2003	196.00	196.00	25.11	07/2009	12/2013	53(O)	0/0
	Total		34,200.81	34,474.24	31,633.81				0/0
Shipping & Ports									
482	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST, Tamil Nadu	06/2005	2,427.40	2,427.40	819.11	10/2008	11/2010	25(O)	0/0
483	DEEPENING OF CHEENEL AT PARADIP PORT - [N25000004]PORT TRUST, Orissa	12/2005	154.84	253.36	221.58	06/2007	12/2010	17(R3)	0/0
484	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM - [N25000015]MUMBAI PORT TRU, Kerala	03/2007	245.67	298.17	297.86	04/2009	12/2010	13(R3)	0/0
485	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU, Maharashtra	11/2007	366.00	366.00	1.43	12/2010	12/2010	0(O)	0/0
486	OPERATION, MANAG. & MAINT. OF MULTI USER-JETTY FOR - [N25000038]PORT TRUST, Karnataka	06/2006	230.00	230.00	-	12/2010	12/2010	0(O)	0/0
487	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]SHIPP., Gujarat	01/2002	165.00	165.00	107.58	12/2005	01/2011	61(O)	0/0
488	C/O Berthing and Allied Facilities off tekra near - [N25000037]PORT TRUST, Gujarat	04/2005	882.00	1,140.00	0.16	02/2011	02/2011	0(O)	0/0
489	ACQUISITION OF 6 NOS. 60470 DWT LR-I PRODUCT TANKE - [N25000029]SHIPP., Maharashtra	10/2006	1,658.59	1,658.59	1,332.47	07/2010	03/2011	8(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
490	ACQUISITION OF 2 NOS. OF 105000 DWT LR-II TANKERS - [N25000030]SHIPP.,Maharashtra	08/2007	586.58	586.58	475.09	11/2010	03/2011	4(O)	0/0
491	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00	755.50	0.73	03/2011	03/2011	0(O)	0/0
492	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44	359.44	273.58	04/2011	04/2011	0(O)	0/0
493	Acquisition of two nos. of 120 B.P - [N25000042]PORT TRUST,Maharashtra	04/2009	290.85	290.85	72.59	03/2011	06/2011	3(O)	0/0
494	ACQUISITION OF 4 NOS. OF 115000 DWT CRUDE OIL CARR - [N25000032]SHIPP.,Maharashtra	08/2008	1,108.12	1,168.42	569.26	04/2011	12/2011	8(O)	0/0
495	Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST,Maharashtra	04/2009	277.03	277.03	55.41	09/2011	12/2011	3(O)	0/0
496	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]SHIPP.,Maharashtra	11/2007	1,061.96	1,061.96	219.98	03/2012	01/2012	-2(O)	0/0
497	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00	3,500.00	-	01/2012	01/2012	0(O)	0/0
498	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00	277.00	-	03/2012	03/2012	0(O)	0/0
499	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91	968.35	222.91	09/2012	08/2012	-1(O)	0/0
500	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10	444.10	-	06/2010	11/2012	29(O)	0/0
501	DEEPENING AND WIDENING OF MAIN HARBOUR CHANNEL AND - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00	800.00	5.22	10/2008	-	-	0/0
502	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]SHIPP.,Tamil Nadu	10/2002	150.00	309.00	23.26	09/2005	-	-	0/0
503	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]PORT TRUST,Kerala	03/2008	375.00	375.00	-	01/2009	-	-	0/0
	Total		17,128.49	17,711.75	4,698.22				0/0
	Telecommunications								
504	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00	1,077.00	841.00	03/2009	09/2010	18(O)	0/0
505	NIB-II PROJECT RURAL BROADBAND - [N26000037]BSNL,Multi State	12/2007	312.86	353.00	234.24	02/2008	09/2010	31(O)	0/0
506	GSM EQUIPMENT OF 1625K LINES(2G) & 325K LINES IN M - [N26000051]BSNL,Madhya pradesh	06/2008	908.30	916.70	151.70	08/2009	09/2010	13(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
507	GSM equipment of 2,00,000Lines (2G) Rajasthan (Ph - [N26000079]BSNL,Rajasthan	09/2009	577.35	577.35	39.86	09/2010	09/2010	0(O)	0/0
508	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00	425.51	109.31	12/2005	10/2010	58(O)	0/0
509	KOLKATA TELECOM DISTRICT PH-4 - [N26000036]BSNL,West Bengal	09/2006	208.50	208.50	146.00	09/2008	10/2010	25(O)	0/0
510	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) - [N26000039]BSNL,Rajasthan	06/2007	601.49	601.49	474.24	12/2008	10/2010	22(O)	0/0
511	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL,Orissa	11/2007	277.34	277.34	293.29	03/2009	10/2010	19(O)	0/0
512	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88	952.88	-	03/2010	10/2010	7(O)	0/0
513	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65	152.65	-	03/2010	10/2010	7(O)	0/0
514	Provision of data network for CWG delhi - [N26000076]MTNL,Delhi	11/2009	488.76	488.76	198.65	10/2010	10/2010	0(O)	0/0
515	GSM equipment of 849862Lines (2G) 150138 lines 3(G - [N26000087]BSNL,West Bengal	02/2008	584.33	584.33	377.08	02/2009	10/2010	20(O)	0/0
516	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL,Jharkhandd	03/2008	328.13	392.44	149.92	03/2009	10/2010	19(O)	0/0
517	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94	373.94	176.33	12/2008	11/2010	23(O)	0/0
518	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]BSNL,Maharashtra	09/2008	1,799.94	1,799.94	214.38	09/2009	11/2010	14(O)	0/0
519	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]BSNL,Uttar Pradesh	05/2007	335.91	335.91	169.43	03/2009	11/2010	20(O)	0/0
520	Procurement of DXC equipment - [N26000074]BSNL,Multi State	02/2008	229.00	229.00	-	03/2010	11/2010	8(O)	0/0
521	GSM equipment of 900000Lines (2G) PunjabPhase V.2 - [N26000081]BSNL,Punjab	09/2008	241.49	241.49	89.66	09/2009	11/2010	14(O)	0/0
522	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84	336.84	22.26	10/2009	11/2010	13(O)	0/0
523	GSM equipment of 975000Lines (2G) 325000 lines 3(G - [N26000083]BSNL,Uttar Pradesh	02/2009	625.53	625.53	242.56	02/2010	11/2010	9(O)	0/0
524	GSM equipment of 1100000Lines (2G) UP East Phase - [N26000084]BSNL,Uttar Pradesh	09/2009	624.75	624.75	75.25	09/2010	11/2010	2(O)	0/0
525	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70	916.70	211.83	11/2010	11/2010	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
526	GSM equipment of 1900000Lines (2G) 401700 lines 3(- [N26000091]BSNL,Tamil Nadu	01/2009	760.20 -	810.37	720.67	01/2010 -	11/2010	10(O)	0/0
527	GSM equipment of 1900000Lines (2G) 335500lines 3(G - [N26000094]BSNL,Kerala	01/2009	848.70 -	848.70	438.75	01/2010 -	11/2010	10(O)	0/0
528	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	384.00	12.64	10/2010 -	11/2010	1(O)	0/0
529	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	247.00	73.73	02/2007 03/2010	12/2010	9(R3)	0/0
530	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	105.16	01/2009 -	12/2010	23(O)	0/0
531	Procurement of 2.5G DWDM equipment - [N26000066]BSNL,Multi State	08/2006	424.00 -	424.00	-	03/2009 -	12/2010	21(O)	0/0
532	Procurement of 10G (40 chl) DWDM equipment - [N26000067]BSNL,Multi State	08/2006	590.10 -	590.10	-	03/2009 -	12/2010	21(O)	0/0
533	Procurement of 10G 40 CHL (12 chl equipped) DWDM - [N26000068]BSNL,Multi State	12/2007	545.50 -	545.50	-	03/2010 -	12/2010	9(O)	0/0
534	Procurement of STM-1 SDH equipment - [N26000069]BSNL,Multi State	02/2007	154.03 -	154.03	-	03/2010 -	12/2010	9(O)	0/0
535	Procurement of STM-16 MADM equipment - [N26000070]BSNL,Multi State	03/2008	355.92 -	355.92	-	03/2010 -	12/2010	9(O)	0/0
536	Procurement of STM-16 ADM equipment - [N26000071]BSNL,Multi State	02/2007	477.00 -	477.00	-	03/2010 -	12/2010	9(O)	0/0
537	Expn of existing 2G & 3G GSM N/W by 750k - [N26000077]MTNL,Maharashtra	10/2008	180.53 -	180.53	40.92	06/2010 12/2010	12/2010	0(R3)	0/0
538	GSM equipment of 375000Lines (2G) 75000lines 3(G) - [N26000085]BSNL,West Bengal	06/2008	170.23 -	167.20	127.42	06/2009 -	12/2010	18(O)	0/0
539	GSM equipment of 945000Lines (2G) 225000lines 3(G) - [N26000086]BSNL,Bihar	10/2007	366.00 -	529.32	202.66	10/2008 -	12/2010	26(O)	0/0
540	GSM equipment of 1867000Lines (2G) 383000 lines 3(- [N26000089]BSNL,Gujarat	08/2008	868.00 -	868.00	274.30	08/2009 -	12/2010	16(O)	0/0
541	GSM equipment of 1700000Lines (2G) 234100 lines 3(- [N26000092]BSNL,Karnataka	10/2008	677.75 719.70	719.70	294.44	10/2009 -	12/2010	14(O)	0/0
542	GSM equipment of 1500000Lines (2G) 264700lines 3(G) - [N26000093]BSNL,Andhra Pradesh	01/2009	922.91 -	922.91	266.06	01/2010 -	12/2010	11(O)	0/0
543	GSM equipment of 614000Lines (2G) 150000lines 3(G) - [N26000095]BSNL,Tamil Nadu	01/2009	315.19 -	315.19	106.18	01/2010 -	12/2010	11(O)	0/0
544	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	229.41	66.20	02/2007 11/2009	03/2011	16(R3)	0/0
545	FTTH BO-3474 /08-09 in Mumbai - [N26000078]MTNL,Maharashtra	09/2011	389.86 -	389.86	2.13	09/2011 -	09/2011	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
546	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38	168.30	94.13	10/2007	-	-	0/0
547	GSM BASED NETWORK EXPANSION PLAN PH-4 - [N26000034]BSNL,Chhatisgarh	02/2007	239.19	239.19	104.48	04/2008	-	-	0/0
548	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 - [N26000040]BSNL,Haryana	01/2008	192.48	192.48	110.88	03/2009	-	-	0/0
549	MANAGED LEASED LINE NETWORK PH-VI - [N26000063]BSNL,Multi State	11/2008	350.00	350.00	-	-	-	-	0/0
550	CENTRALISED TRANSMISSION NMS - [N26000064]BSNL,Multi State	08/2009	300.00	300.00	-	-	-	-	0/0
	Total		22,779.47	23,237.57	7,257.74				0/0
	Urban Development								
551	DELHI MRTS PHASE-II PROJECT - [280100002]DMRC,Delhi	08/2005	8,676.00	18,894.36	15,839.63	06/2010	10/2010	4(O)	0/8
552	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00	11,609.00	2,954.59	12/2011	03/2013	15(O)	6/6
	Total		15,071.00	30,503.36	18,794.22				6/14
	Water Resources								
553	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90	1,187.00	35.49	12/2007	12/2012	60(O)	0/0
	Total		542.90	1,187.00	35.49				0/0
Grand Total			569,479.67	691,003.22	285,920.13				802/2191


Sector wise Current Status of Projects on the Flash Report

1. Sector: - Atomic Energy

Number of Projects	4
Number of Projects Wo_Odc_Original	1
Number of Projects Delayed	3

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 1 projects are Wo_Odc_Original and 3 projects are delayed.

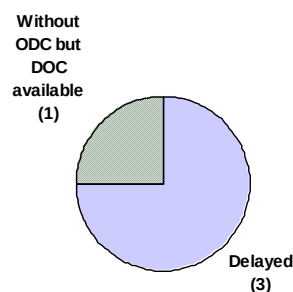

Investment Scenario

Figures are in Rs. Crores

The total cost of implementation of 4 projects when sanctioned, was of the order of Rs. 21982.29 Crores but this was subsequently revised to Rs. 23236.29 Crores. The expenditure incurred on these projects till Sept, 2010 is Rs. 19092.89 Crores.

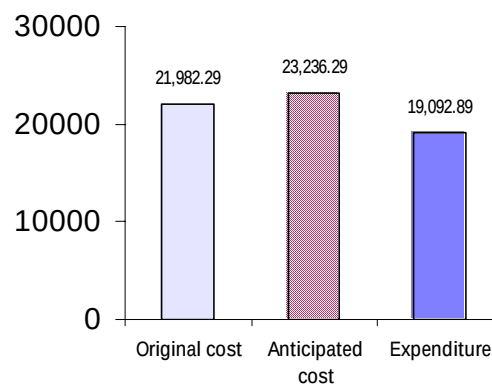


2. Sector: - Civil Aviation

Number of Projects	9
Number of Projects on schedule	3
Number of Projects Delayed	3
Number of Projects Wo_Doc_Original	3


Brief Analysis

Project Status with respect to Original Schedule: Out of 9 projects, 3 projects are on schedule, 3 projects are delayed and 3 projects are original date of commissioning.



Investment Scenario

The total cost of implementation of 9 projects when sanctioned, was of the order of Rs. 5347.40 Crores but this was subsequently revised to Rs. 5347.40 Crores. The expenditure incurred on these projects till Sept, 2010 is Rs 2522.61 Crores.

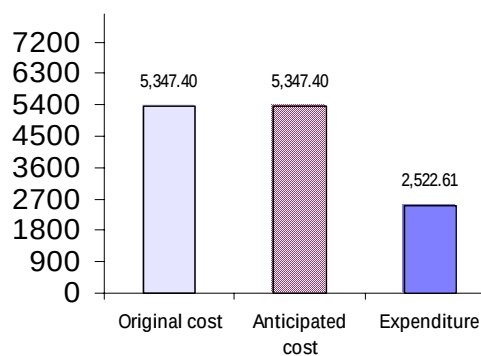


3. Sector: - Coal

Number of Projects	44
Number of Projects on schedule	13
Number of Projects Delayed	19
Number of Projects Ahead	3
Number of Projects Wo_ODC_Original	8
Number of Projects Wo_DOC_Original	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 44 projects, 13 projects are on schedule, 19 projects are delayed and 3 projects are ahead and 8 Project W_Odc_Original and 1 Project W_Odc_Original .



Investment Scenario

The total cost of implementation of 44 projects when sanctioned, was of the order of Rs. 25210.30 Crores but this was subsequently revised to Rs. 28542.29 Crores. The expenditure incurred on these projects till Sept, 2010 is Rs 10123.40 Crores

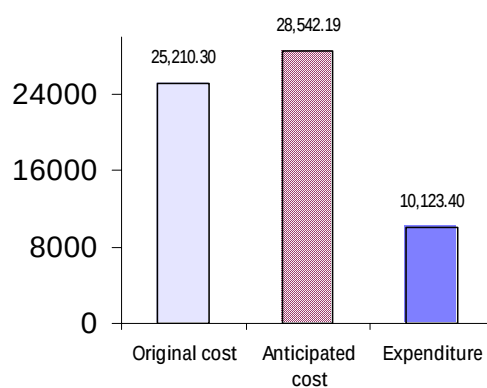


4. Sector: - Petroleum

Number of Projects	70
Number of Projects on schedule	29
Number of Projects Delayed	32
Number of Projects Ahead	3
Number of Projects Wo_Doc_Original	1
Number of Projects Without original date of commissioning	5


Brief Analysis

Project Status with respect to Original Schedule: Out of 70 projects, 29 projects are on schedule, 32 projects are delayed and 3 projects are ahead and 1 projects is without date of commissioning and 8 Project is Without original date of commissioning.

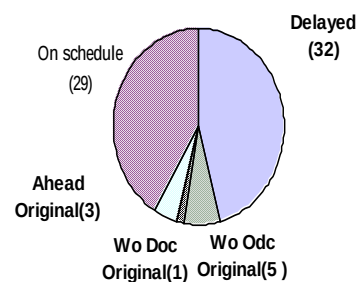

Investment Scenario

The total cost of implementation of 70 projects when sanctioned, was of the order of Rs. 144690.62 Crores but this was subsequently revised to Rs. 160094.89 Crores. The expenditure incurred on these projects till Sept, 2010 is Rs. 45689.10 Crores.

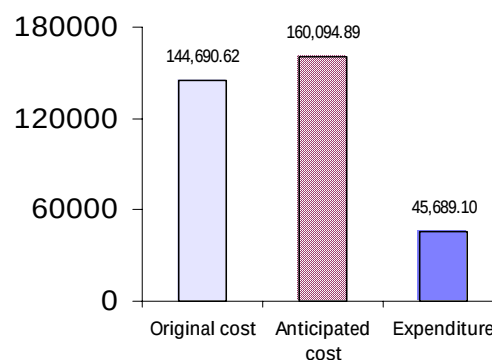


5. Sector: - Power


Number of Projects	85
Number of Projects on schedule	37
Number of Projects Delayed	38
Number of Projects Ahead	5
Number of Projects Wo_Doc_Original	4
Number of Projects Wo_Odc_Original	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 85 projects, 40 projects are on schedule, 35 projects are delayed, and 5 Projects are Ahead, 4 projects are without date of commissioning and 1 projects is with out original date of commissioning

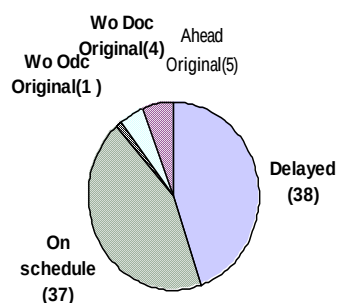

Investment Scenario

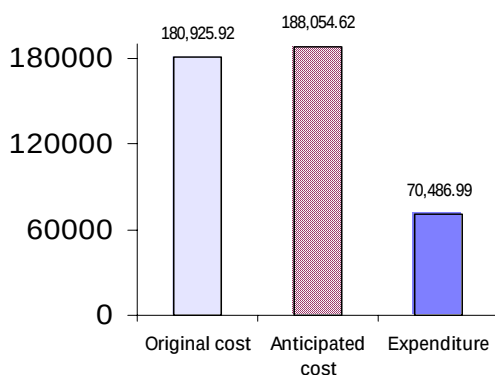


The total cost of implementation of 85 projects when sanctioned, was of the order of Rs. 180925.92 Crores but this was subsequently revised to Rs. 188054.62 Crores. The expenditure incurred on these projects till Sept, 2010 is Rs. 70486.99 Crores.

6. Sector: - Railways

Number of Projects	129
Number of Projects on schedule	5
Number of Projects Delayed	25
Number of Projects Ahead	2
Number of Projects Wo_Doc_Original	61
Number of Projects Wo_Odc_Original	36


Brief Analysis

Project Status with out respect Original Schedule: Out of 129 projects, 5 projects are on schedule, 25 projects are delayed, 2 projects is ahead. 61 projects are Without date of commissioning and 36 projects are without original date of commissioning.

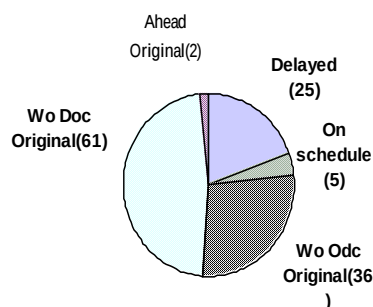

Investment Scenario

The total cost of implementation of 129 projects when sanctioned, was of the order of Rs. 49023.84 Crores but this was subsequently revised to Rs. 104193.13 Crores. The expenditure incurred on these projects till Sept, 2010 is Rs. 45786.84 Crores.

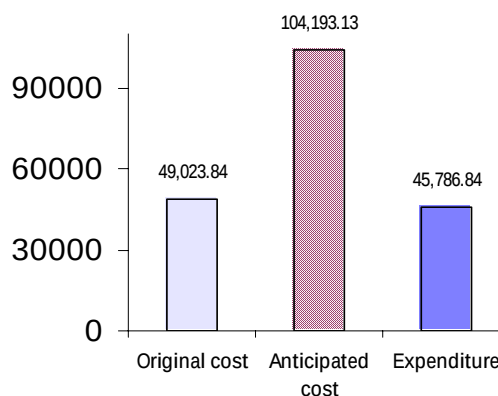


7. Sector: - Road Transport and Highways

Number of Projects	116
Number of Projects on schedule	3
Number of Projects Delayed	113


Brief Analysis

Project Status with respect to Original Schedule: Out of 116 projects, 3 projects are on schedule, 113 projects are delayed.



Investment Scenario

The total cost of implementation of 116 projects when sanctioned, was of the order of Rs 34200.81 Crores but this was subsequently revised to Rs. 34474.24 Crores. The expenditure incurred on these projects till Sep, 2010 is Rs. 31633.81 Crores.

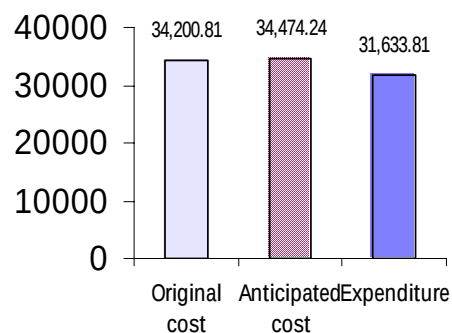


8. Sector: - Shipping and Ports

Number of Projects	22
Number of Projects on schedule	7
Number of Projects Delayed	10
Number of Projects Ahead	2
Number of Projects Wo_Doc_Original	3


Brief Analysis

Project Status with respect to Original Schedule: Out of 22 projects, 7 projects are on schedule, 10 projects are delayed, 2 projects are ahead and 3 projects are without date of commissioning.

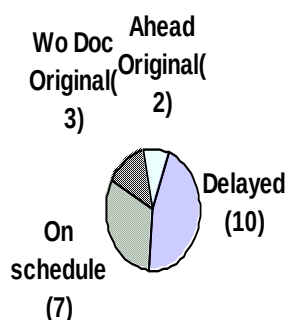

Investment Scenario

The total cost of implementation of 22 projects when sanctioned, was of the order of Rs.17128.49 Crores but this was subsequently revised to Rs. 17711.75 Crores. The expenditure incurred on these projects till Sep, 2010 is Rs. 4698.22 Crores.

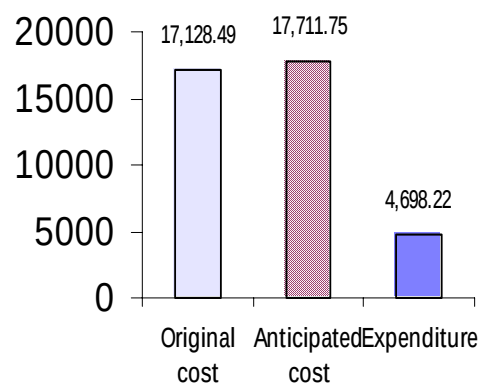


9. Sector: - Steel

Number of Projects	16
Number of Projects Delayed	7
Number of Projects Ahead Original	1
Number of Projects Wo_Doc_Original	4
Number of Projects On schedule	4


Brief Analysis

Project Status with respect to Original Schedule: Out of 16 projects, 7 projects are delayed and 4 projects are on Schedule and 4 projects are Wo_Doc_Original and 1 Project is ahead.

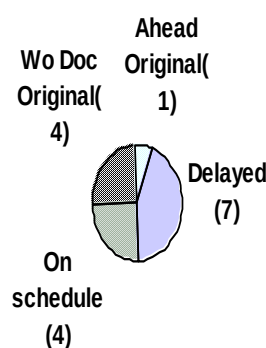

Investment Scenario

The total cost of implementation of 20 projects when sanctioned, was of the order of Rs.43098.53 Crores but this was subsequently revised to Rs. 64258.46 Crores. The expenditure incurred on these projects till Sep, 2010 is Rs. 25232.58 Crores.

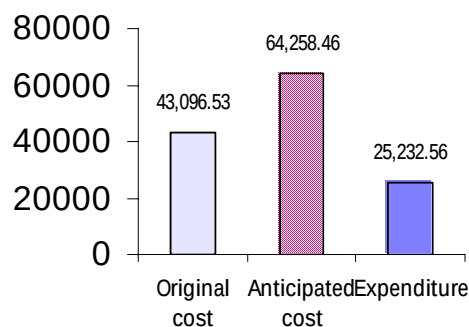


10. Sector: - Telecommunications

Number of Projects	47
Number of Projects Delayed	38
Number of Projects on Schedule	4
Number of Projects Wo_Doc_Original	5


Brief Analysis

Project Status with respect to Original Schedule: Out of 47 projects, 38 projects are delayed and 5 projects are with out date of commissioning, and 4 projects are on schedule.

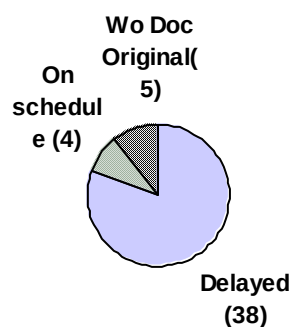

Investment Scenario

The total cost of implementation of 47 projects when sanctioned, was of the order of Rs 22779.47 Crores but this was subsequently revised to Rs. 23237.57 Crores. The expenditure incurred on these projects till Sep, 2010 is Rs 7257.74 Crores.

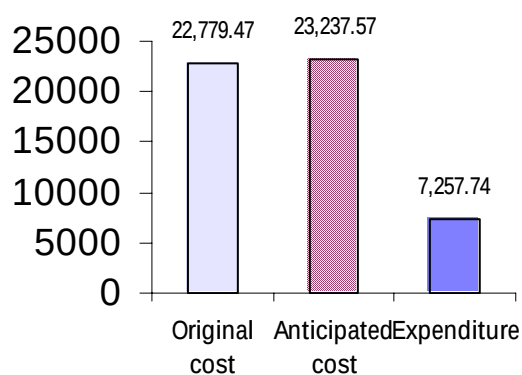

STATE WISE PROJECTS AS ON 30.09.2010

SN	STATE_NAME	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	EXPENDITURE CUMM
	Andhra Pradesh	35	28652.64	35503.31	17316.17
	Arunachal Pr.	4	12009.12	13180.26	6847.35
	Assam	40	23365.64	28500.60	10486.29
	Bihar	31	29643.83	32782.54	17210.34
	Chhatisgarh	17	20642.28	35617.35	12597.26
	Delhi	3	9413.76	19612.53	16104.48
	Goa	1	204.73	204.73	5.97
	Gujarat	20	13416.98	16549.86	9800.34
	Haryana	11	4780.87	5449.61	2288.28
	Himachal Pr.	8	15381.72	15463.96	10102.42
	J & K	9	8963.30	19472.26	10575.70
	Jharkhandd	21	9761.89	14698.51	4975.65
	Karnataka	18	15490.06	22957.00	10595.15
	Kerala	11	9511.93	11042.22	5713.50
	Madhya pradesh	26	19323.72	19588.25	6748.41
	Maharashtra	50	65486.21	84795.62	27078.36
	Manipur	1	578.62	578.62	28.33
	Meghalaya	1	71.18	443.15	547.78
	Mizoram	2	988.06	3343.04	218.40
	Multi State	93	112382.36	116242.43	28825.89
	Orissa	25	48184.60	52134.37	13603.95
	Punjab	11	5532.97	6388.00	2781.33
	Rajasthan	10	8832.80	9560.86	5753.32
	Sikkim	2	1603.77	3644.86	2.56
	Tamil Nadu	32	39822.61	45724.94	31755.38
	Tripura	3	1522.39	1724.82	156.65
	Uttar Pradesh	39	24151.87	26070.62	10554.54
	Uttaranchal	8	11951.31	14505.03	3989.84
	West Bengal	21	30305.35	37720.77	20485.93
TOTAL		553	571976.57	693500.12	287149.57

Abbreviations used in the report

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro
LEP	Life Extension Program
LOI	Letter of Intent

LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SSS	Sardar Swaran Singh
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TPY	Tonnes per year
UG	Under Ground
ULDSCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
