

**306th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹.150 Crores and above)
April, 2011**



Construction activity at Kosi Bridge



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Contents

Executive Summary	1 -5
Month wise list of completed projects Costing Rs. 150 Crore and Above During 2010-11	6-12
List of Delete Projects	13
Summary of Projects	14-24
Sector wise Trend and Graphicalf Analysis	25-37
Sector wise analysis of projects	38-67
Graph	68-78
Statewise Summary of All Ongoing Projects	79
List of Abbreviations	80-81

EXECUTIVE SUMMARY

The Flash Report for April 2011 (the 306th Flash Report) contains information on the status of the 560 projects in the Central Sector costing ` 150 Crores and above. During April 2011, seven projects have reported completion (which have now been dropped from the monitor of this Ministry).

The online submission of the implementation Status Report of the ongoing projects from the project authorities has improved considerably with all projects reporting online during the current month. This has been mainly due to the continuous effort/persuasion by this Ministry. During April 2011, forty six (46) projects have reported additional delays compared to the completion dates in the previous month. The additional delays are in the range of 1 to 36 months in respect of projects relating to Coal, Steel, Petroleum, Power, Railways, Road Transport and Highways, Civil Aviation, Mines and Atomic Energy Sectors.

S. No.	Sector	Projects on monitor	Additional delays
1.	ROAD TRANSPORT & HIGHWAYS	119	13
2.	RAILWAYS	139	5
3.	POWER	86	8
4.	PETROLEUM	73	10
5.	COAL	45	3
6.	TELECOMMUNICATION	41	0
7.	STEEL	13	3
8.	SHIPPING & PORTS	23	0
9.	CIVIL AVIATION	7	2
10.	FERTILISERS	6	0
11.	ATOMIC ENERGY	3	1
12.	URBAN DEVELOPMENT	3	0
13.	MINES	1	1
14.	WATER RESOURCES	1	0
Total		560	46

3. The total original cost of implementation of the 560 projects was about ` 6,03,783.35 Crores and their anticipated completion cost is likely to be ` 7,28,399.46 Crores, which reflects an overall cost overrun of 20.60%. The expenditure incurred on these projects till April, 2011 is ` 3,21,667.26 Crores.

4. Out of the 560 projects, 10 projects are ahead of schedule, 137 are on schedule and 251 projects are delayed and 116 projects have been sanctioned without any commissioning schedule/date. Further in case of 46 projects neither the year of commissioning nor the tentative gestation period of the projects have been reported but subsequently date of completion have been finalised. The concerned ministries have been requested to fix the date of commissioning of their projects at an early date.

5. During the month the project reporting delays have marginally decreased to 251 from 264 in March'2011. The overall cost overrun has also increased to 20.60% from 19.70% in March 2011. Out of 251 delayed projects, at the end of April, 2011, 60 projects had overall delay in the range of 1 to 12 months, 53 projects had delay in the range of 13 to 24 months, 106 projects had delay in the range of 25 to 60 months and 32 projects had delay of 61 months and above.

The Sector-wise details of delays are as under:-

i) In the **Coal sector**, 3 projects have reported additional delays in the range of 2-36 months. Adriyala Shaft Project SCCL has reported an improvement of one month. Tuticorin Thermal Power Project, NLC has reported additional delay of two months due to inadequate mobilization by the contractor. RKP OCP Phase – 1 SCCL has reported additional delay of 36 months due to delay in acquisition of forest & private land .

ii) In the **Steel sector**, 3 projects have reported additional delays in the range of 1-3 months. Rebuilding of Coke Oven Battery No-6 ,Bokaro Steel Plant, SAIL and 67.5 MW TG-5 Auxiliary System Emergency Power Requirement project, RINL have reported an additional delay of one month each due to delay in supply of fireclay & silica brick by the contractor. 330 TPH Boiler-6 and Auxiliary System, RINL has reported an additional delay of 3 months due to increased cost of labour charge.

iii) In the **Petroleum Sector**, 10 projects have reported additional delays in the range of 1-12 months. BNPL Superlines (Uttranchal & Punjab) of GAIL has reported additional delay of 6

months due to delay for permission from Supreme Court is required to lay pipeline in Raja ji National Park & it will take one year to obtaining permission. Resitement of Marketing Installation at Visakhapatnam HPCL, C2-C3 and LPG Recovery from LNG Dahej ONGC, Diesel Hydro Treatment Project Dhaligaon BRPL, Heera Reconstruction ONGC, Neelam Reconstruction ONGC, Compressor Stations (Kailaras & Chains) Gail, VKPL Upgradation and laying of spurline to Bhilwara and Chai GAIL, Dhabol-Bangalore Pipeline Project Phase-1 GAIL and Kochi – Kanjirkod Bangalore-Mangalore Pipeline Project Phase-1 GAIL have reported an additional delay of one month, 2 months, 2 months, 2 months, 2 months, 3 months, 3 months, 5 months and 12 months respectively, However no specific reason has been reported by the Project authorities.

iv) In the Power Sector, 8 projects have reported additional delays in the range of 1-12 months. Northern Region System Strengthening Scheme-XV PGCIL and Northern Region System Strengthening Scheme-XVII PGCIL have reported an additional delay of 3 months and 6 months due to delay in land acquisition in sub service station. Bongaigaon Thermal Power Project NTPC has reported an additional delay of 6 months due to delay in turbo generator erection and slow progress by civil agency. Nimoo Bazgo Hydroelectric Project NHPC has reported an additional delay of 9 months due to highly inclement weather conditions of Leh Ladakh and frequent bandhs/strikes. Transmission System for Startup Power to DVC & Maithon RBG PGCIL, Transmission System Associated with Krishnapatnam PGCIL, System Strengthening-XI in Southern Region PGCIL and Vishnugad Pipalkoti Hydro Electric Project THDCL have reported an additional delay of 1 month, 6 months, 7 months and 12 months respectively, However no specific reason has been reported by the project authorities.

v) In the Road Transport and Highways Sector, 13 projects have reported additional delay in the range of 1-12 months. 8 projects have reported additional delay of one month each due to slow progress of work by the contractor. Ganjam-Icchapuram, NH-5, NHAI has reported additional delay of 2 months due to delay in utility shifting. Kurali Kiratpur NH- 21, NHAI has reported additional delay of 2 months due to slow mobilization by the contractor. Balasore Bhadrak (Revived) KM 136.5-199.14) NH-5 NHAI has reported additional delay of 2 months due to delay in handing over of land in some portions . End of Durg Bypass has reported additional delay of 2 months due to delay in removal of encroachments. Gwalior Bypass, NH-75, NHAI has reported an additional delay of 12 months due to non-availability of defence land.

vi) In the **Mines Sector**, Second Phase Expansion of Captive Aluminum, Smelter and Power NALCO has reported an additional delay of two months due to delay in sequential release of drawings by the consultants.

vii) In the **Railway Sector**, 5 projects have reported additional delay in the range of 2-23 months. Ghutiarisharif- Canning ER has reported an additional delay of 2 months due to encroachment and delay in land acquisition. Kosi Bridge (NL) ECR has reported an additional delay of 9 months as work suffered due to river training work being executed by NHAI. Katakhal to Bhairabi NEFR and Dakshin-Barasat-Lakshmikantapur ER have reported an additional delay of 12 months and 23 months due to delay in land acquisition. Chhindwara – Nagpur (GC) SECR has reported an additional delay of 18 months, however no specific reason has been reported by the project authority.

viii) In the **Atomic Energy Sector**, Uranium ORE Mine & Processing Plant at Tummalapalli UCIL has an additional delay of 4 months due to political disturbance on Telangana issue and non-availability of skilled construction labour.

ix) In the **Civil Aviation Sector**, 2 projects have reported additional delay in the range of 9-17 months. Development of Kamraj Domestic Terminal Phase- II & Expansion of Anna International Terminal (K1) AAI and Construction of new Airport at Pakyong (Sikkim) Airport AAI have reported an additional delay of 9 months and 17 months, however no specific reason has been reported by the Project authority.

The status as on 01.05.2011 in respect of completion of projects costing ` 150 Crores and above in different sectors during 2011-12 is indicated in the Report.



(Pankaj Jain)
Additional Secretary
Ministry of Statistics & Programme Implementation

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Additional Delayed
1	Railways	139	5
2	Road Transport & Highways	119	13
3	Power	86	8
4	Petroleum	73	10
5	Coal	45	3
6	Telecommunications	41	0
7	Shipping & Ports	23	0
8	Steel	13	3
9	Civil Aviation	7	2
10	Fertilisers	6	0
11	Atomic Energy	3	1
12	Urban Development	3	0
13	Mines	1	1
14	Water Resources	1	0
	Total	560	46

ANNEXURE-I

Month wise List of Completed Project Costing Rs. 150 Crore and above during 2011-2012

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
April,2011				
<u>Civil Aviation</u>				
1	Extension of Secondary Runway(K2)(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000056]	230.00	01/2011	241.28
<u>Petroleum</u>				
2	SULTANPUR NEEMRANA PIPE LINE PROJECT (Spurline to CJPL)(GAS AUTHORITY OF INDIA LIMITED) - [N16000049]	396.13	10/2009	106.22
3	Guru Govind Singh Refinery Products Evacuation Project(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000076]	605.40	12/2010	408.90
<u>Power</u>				
4	Farakka STPP Stage-III(NATIONAL THERMAL POWER CORPORATION) - [N18000016]	2,570.44	08/2010	1,896.00
<u>Railways</u>				
5	GUNTUR-GUNTAKAL-KALLURU(GL)(SCR)(SOUTH CENTRAL RAILWAY) - [220100330]	458.45	-	555.49
<u>Road Transport & Highways</u>				
6	MADURAI -KANIAKUMARI SECTION (NS-41/TN) NH-7,KM.80 TO KM.120(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106240]	323.36	03/2008	189.90
<u>Shipping & Ports</u>				
7	ACQUISITION OF 4 NOS. OF 115000 DWT CRUDE OIL CARR(SHIPPING corp. of india) - [N25000032]	1,108.12	04/2011	374.36

Summary of projects in the Flash Report for the month of April, 2011


I. Project Implementation - Current Status:

Number of Projects in Previous Month	579
Number of Projects completed/dropped/frozen in Previous Month	17
Number of Projects completed/dropped/frozen in Current Month	9
Number of Projects with Anticipated greater than Rs. 150 Cr. in Current Month	7

Number of Projects in Current Month **560**

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 560 projects, 10 projects are ahead of schedule, 137 projects are on schedule and 251 projects are delayed. Of the balance, 116 projects do not have fixed dates of commissioning while 46 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

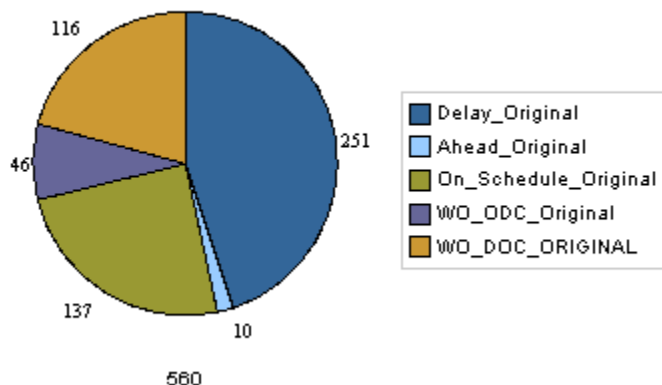

III. Investment Scenario

The Total Original cost of implementation of 560 projects when sanctioned, was of the order of Rs. 603783.35 crore but this was subsequently revised to Rs. 728399.46 crore implying a cost overrun of 20.6%. The expenditure incurred on these projects till April, 2011 is Rs. 321667.26 crore, which is 44.2% of the revised cost of the projects.

Figures are in Rs. Crore

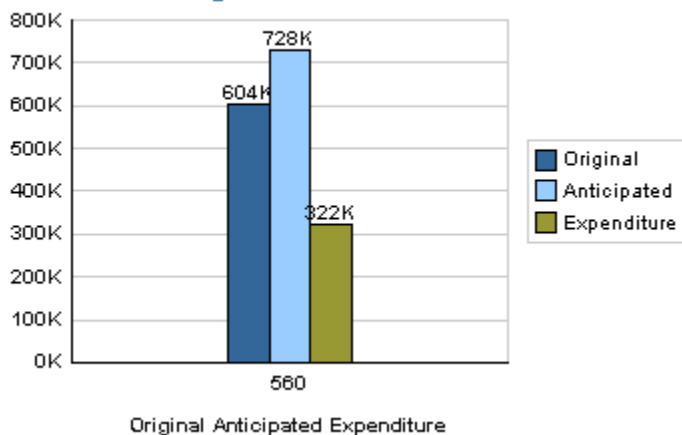

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	579
No of Projects Completed/Dropped/Frozen in Previous Month	17
No of Projects Completed/Dropped/Frozen in Current Month	9
No of Projects with Anticipated Cost Greater than Rs.150 Cr. In Current Month	7
No of Projects added in Current Month	0
No of Projects in Current Month	560

II. Project status

With Respect To	Number of Projects					Total	Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C		
Original (Date)	251	10	137	46	116	560	44.82
Latest Approved (Date)	263	11	187	29	71	560	46.96

III. (A) Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	448	500,918.09	551,019.50	225,401.37	40.90	50,101.41	10.00
Latest Approved (RCE)	112	152,948.69	177,379.96	96,265.89	54.30	24,431.27	16.00
Total (RCE)	560	653,866.78	728,399.46	321,667.26	44.16	74532.68	11.40
Original Cost of All Projects							
Original Cost	560	603,783.35	728,399.46	321,667.26	44.20	124,616.11	20.60

III. (B) Delayed Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	251	299,194.33	369,361.63	217,976.52	59.00	70,167.30	23.50
Latest Approved (RCE)	263	287,923.72	338,647.11	197,184.80	58.20	50,723.39	17.60

IV. Additional Delayed Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Latest Approved	46	38,771.27	37,907.12	22,590.38	59.60	-864.15	-2.20

Extent of cost overrun in projects with respect to original schedule

S.No.	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Original	Anticipated cost	Cost overrun (%)	No .	Original cost	Anticipated cost	% Incr Base
1	Atomic Energy	3	17,769.3	22,607.3	27.2	2	16,663.0	21,501.0	29.0
2	Civil Aviation	7	4,826.5	4,826.5	0.0	0	0.0	0.0	0.0
3	Coal	45	25,509.2	28,789.5	12.9	8	7,550.9	11,526.8	52.7
4	Fertilisers	6	5,317.4	5,317.4	0.0	0	0.0	0.0	0.0
5	Mines	1	4,091.5	4,401.8	7.6	1	4,091.5	4,401.8	7.6
6	Steel	13	39,927.9	65,040.9	62.9	10	24,811.2	49,924.2	101.2
7	Petroleum	73	157,868.4	167,285.0	6.0	19	28,691.1	46,288.0	61.3
8	Power	86	178,558.2	184,085.6	3.1	12	17,694.7	23,696.0	33.9
9	Railways	139	66,776.0	123,021.2	84.2	104	37,098.0	93,438.5	151.9
10	Road Transport & Highways	119	52,920.8	54,384.2	2.8	11	3,482.9	5,515.4	58.4
11	Shipping & Ports	23	14,464.2	15,317.7	5.9	6	3,346.8	4,401.4	31.5
12	Telecommunications	41	20,026.0	21,450.8	7.1	9	3,362.9	4,870.4	44.8
13	Urban Development	3	15,185.2	30,684.7	102.1	3	15,185.2	30,684.7	102.1
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		560	603,783.4	728,399.5	20.6	186	162,521.1	297,435.1	83.0

Extent of the time overrun in projects with respect to original schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	3	17,769.3	22,607.3	27.2	2	16,663.0	21,501.0	16 - 39
2	Civil Aviation	7	4,826.5	4,826.5	0.0	3	3,479.8	3,479.8	3 - 17
3	Coal	45	25,509.2	28,789.5	12.9	22	17,959.7	20,789.4	2 - 48
4	Fertilisers	6	5,317.4	5,317.4	0.0	1	1,478.6	1,478.6	1 - 1
5	Mines	1	4,091.5	4,401.8	7.6	1	4,091.5	4,401.8	29 - 29
6	Steel	13	39,927.9	65,040.9	62.9	5	29,941.7	39,219.7	15 - 29
7	Petroleum	73	157,868.4	167,285.0	6.0	34	46,664.0	56,611.7	2 - 120
8	Power	86	178,558.2	184,085.6	3.1	44	106,786.7	111,962.5	2 - 90
9	Railways	139	66,776.0	123,021.2	84.2	22	17,342.2	37,477.7	2 - 213
10	Road Transport & Highways	119	52,920.8	54,384.2	2.8	97	32,468.7	33,112.1	1 - 90
11	Shipping & Ports	23	14,464.2	15,317.7	5.9	14	5,824.5	6,776.5	2 - 72
12	Telecommunications	41	20,026.0	21,450.8	7.1	3	880.0	860.4	6 - 54
13	Urban Development	3	15,185.2	30,684.7	102.1	2	15,071.0	30,503.4	12 - 15
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	60 - 60
Total		560	603,783.4	728,399.5	20.6	251	299,194.3	369,361.6	

Extent of time & cost overrun in projects with respect to original schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	3	17,769.29	22,607.29	27.23	2	16,663.00	21,501.00	16- 39
2	Civil Aviation	7	4,826.48	4,826.48	0.00	0	0.00	0.00	0- 0
3	Coal	45	25,509.15	28,789.48	12.86	7	6,813.24	10,338.47	3- 48
4	Fertilisers	6	5,317.41	5,317.41	0.00	0	0.00	0.00	0- 0
5	Mines	1	4,091.51	4,401.76	7.58	1	4,091.51	4,401.76	29- 29
6	Steel	13	39,927.85	65,040.88	62.90	2	14,825.00	24,103.00	25- 29
7	Petroleum	73	157,868.41	167,284.98	5.96	18	26,137.79	42,491.76	2- 120
8	Power	86	178,558.19	184,085.59	3.10	11	17,098.27	22,748.04	3- 90
9	Railways	139	66,775.98	123,021.21	84.23	18	10,707.60	31,186.83	12- 213
10	Road Transport & Highways	119	52,920.82	54,384.23	2.77	10	2,374.90	3,227.40	25- 90
11	Shipping & Ports	23	14,464.19	15,317.65	5.90	6	3,346.84	4,401.36	6- 72
12	Telecommunications	41	20,025.99	21,450.84	7.12	7	2,274.59	3,165.48	17- 58
13	Urban Development	3	15,185.18	30,684.66	102.07	3	15,185.18	30,684.66	12- 21
14	Water Resources	1	542.90	1,187.00	118.64	1	542.90	1,187.00	60- 60
Total		560	603783.35	728399.46	20.64	86	120060.82	199436.76	

V. List of projects completed/dropped/Frozen current month

(All Cost /Expenditure in Rs. crore)

Project	DOA	Original		Now anticipated		Final
		Cost	DOC	Cost	DOC	Expenditure
<u>Power</u>						
TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI = II HEP	12/2005	358.42	12/2008	358.42	12/2012	5.49
<u>Railways</u>						
GUNTUR-GUNTAKAL-KALLURU(GL)(SCR)	04/1992	458.45	N.A.	573.12	N.A.	555.49
<u>Road Transport & Highways</u>						
MADURAI -KANIAKUMARI SECTION (NS-41/TN) NH-7,KM.80 TO KM.120	12/2003	323.36	03/2008	323.36	04/2011	189.90
<u>Petroleum</u>						
SULTANPUR NEEMRANA PIPE LINE PROJECT (Spurline to CJPL)	11/2007	396.13	10/2009	266.00	04/2011	106.22
JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I	07/2009	7,596.18	03/2012	6,652.22	N.A.	.50
<u>Power</u>						
Farakka STPP Stage-III	07/2006	2,570.44	08/2010	2,570.44	03/2011	1,896.00
<u>Shipping & Ports</u>						
ACQUISITION OF 4 NOS. OF 115000 DWT CRUDE OIL CARR	08/2008	1,108.12	04/2011	1,238.88	03/2011	374.36
<u>Petroleum</u>						
Guru Govind Singh Refinery Products Evacuation Project	01/2009	605.40	12/2010	510.00	12/2010	408.90
<u>Civil Aviation</u>						
Extension of Secondary Runway(K2)	08/2008	230.00	01/2011	230.00	N.A.	241.28

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
<u>Atomic Energy</u>						
URANIUM ORE MINE & PROCESSING PLANT AT TUMMALAPALL UCIL	1,106.29	1,106.29	N.A.	12/2011	04/2012	4
<u>Civil Aviation</u>						
D/O KAMARAJ DOMESTIC TER-PH-II & EXP. ANNA INT. TE(K1) AAI	1,273.00	1,273.00	01/2011	01/2011	10/2011	9
C/o new Airport at Pakyong(Sikkim) Airport AAI	264.29	264.29	01/2011	01/2011	06/2012	17
<u>Coal</u>						
ADRIYALA SHAFT PROJECT SCCL	212.34	779.26	03/2013	07/2013	06/2013	-1
TUTICORIN THERMAL POWER PROJECT NLC	4,909.54	4,909.54	08/2012	08/2012	10/2012	2
RKP OCP PHASE-I SCCL	209.78	209.78	03/2015	03/2015	03/2018	36
<u>Mines</u>						
SECOND PHASE EXPANSION OF CAPTIVE ALUMINIUM,SMELTER AND POWE NALCO	4,091.51	4,401.76	12/2008	03/2011	05/2011	2
<u>Steel</u>						
REBUILDING OF COKE OVEN BATTERY NO-6 (BSP) SAIL	172.78	172.78	01/2010	06/2011	07/2011	1
67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREM RINL	230.00	343.58	N.A.	08/2011	09/2011	1
330 TPH BOILER-6 AND AUXILIARY SYSTEM RINL	260.00	350.00	N.A.	06/2011	09/2011	3
<u>Petroleum</u>						

VIII. List of projects reporting additional delays


Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT HPCL	756.00	756.00	12/2011	08/2011	09/2011	1
C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC) ONGC	900.92	976.08	05/2008	02/2011	04/2011	2
DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON BRPL	1,431.91	1,690.13	09/2009	04/2011	06/2011	2
HEERA RECONSTRUCTION ONGC	706.70	706.70	04/2010	04/2011	06/2011	2
NEELAM RECONSTRUCTION ONGC	305.08	305.08	04/2011	04/2011	06/2011	2
COMPRESSOR STATIONS (KAILARAS &CHAINS) GAIL	1,167.00	810.00	04/2011	09/2011	12/2011	3
VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI GAIL	463.32	340.00	06/2011	12/2011	03/2012	3
DHABOL-BANGALORE PIPELINE PROJECT PHASE-I GAIL	4,543.43	2,500.00	03/2012	03/2012	08/2012	5
BNPL SPURLINE (UTTRANCHAL & PUNJAB) GAIL	540.92	400.00	06/2011	01/2012	07/2012	6
KOCHI-KANJIRKOD BANGALORE-MANGALORE PIPELINE PROJECT PHASE-I GAIL	348.00	260.00	03/2012	12/2011	12/2012	12
Power						
TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB G PGCIL	290.49	299.08	04/2010	04/2011	05/2011	1
NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV PGCIL	520.48	520.48	11/2011	11/2011	02/2012	3
BONGAIGAON THERMAL POWER PROJECT (NTPC) NTPC	4,375.35	4,375.35	07/2011	04/2013	10/2013	6
NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII PGCIL	210.79	210.79	08/2011	08/2011	02/2012	6
TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM PGCIL	779.21	779.21	08/2013	11/2012	05/2013	6
SYSTEM STRENGTHENING - XI IN SOUTHERN REGION PGCIL	196.10	196.10	07/2011	07/2011	02/2012	7
NIMOO BAZGO HYDROELECTRIC PROJECT (NHPC) NHPC	611.02	611.02	08/2010	09/2011	06/2012	9

VIII. List of projects reporting additional delays


Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT THDCL	2,221.31	2,491.58	07/2014	03/2015	03/2016	12
<u>Railways</u>						
Ghutarisharif-Canning (ER) ER	189.97	189.97	12/2011	12/2011	02/2012	2
KOSI BRIDGE (NL), ECR ECR	323.41	341.41	N.A.	03/2012	12/2012	9
Katakhal to Bhairabi NEFR	227.90	227.90	12/2012	12/2012	12/2013	12
CHHINDWARA - NAGPUR (GC)(SECR) SECR	383.79	585.93	N.A.	06/2012	12/2013	18
Dakshin-barasat- lakshmikantapur (ER) ER	259.51	259.51	12/2011	12/2011	11/2013	23
<u>Road Transport & Highways</u>						
PURNEA-GOYAKOTA SEC.(EW) (NS & EW-PH-I) KM.419-KM.447, NH-31 NHAI	205.73	205.73	07/2004	04/2011	05/2011	1
IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS NHAI	210.00	210.00	04/2007	04/2011	05/2011	1
MADURAI-ARUPKOTTAI- TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B NHAI	629.00	629.00	11/2010	04/2011	05/2011	1
NAGAON BYPASS (NH- 37)(NHAI) NHAI	230.00	230.00	06/2008	04/2011	05/2011	1
KOTA BYPASS,RJ-4, NH-76 (NHAI) NHAI	275.00	250.39	10/2008	04/2011	05/2011	1
THRISSUR TO ANGAMALI (NH-47) NHAI	312.50	312.50	03/2009	04/2011	05/2011	1
TRICHY - DINDIGUAL NH-45 NHAI	576.00	576.00	07/2010	04/2011	05/2011	1
PONDICHERY - TINDIVANAU NH-66 NHAI	285.00	285.00	07/2010	04/2011	05/2011	1
GANJAM-ICCHAPURUM,NH- 5(NHAI) NHAI	263.27	263.27	02/2004	04/2011	06/2011	2
KURALI-KIRATPUR, NH-21 NHAI	309.00	309.00	06/2010	04/2011	06/2011	2
BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 NHAI	228.70	228.70	02/2004	04/2011	06/2011	2
END OF DURG BYPASS- CHHATISGARH/MAHARASHT RA BORDER NHAI	464.00	464.00	01/2011	04/2011	06/2011	2
GWALIOR BYPASS, NH-75,3 NHAI	300.93	300.93	10/2009	06/2011	06/2012	12

Number of projects reporting additional delay = 46


Trend and Graphical Analysis of All Projects

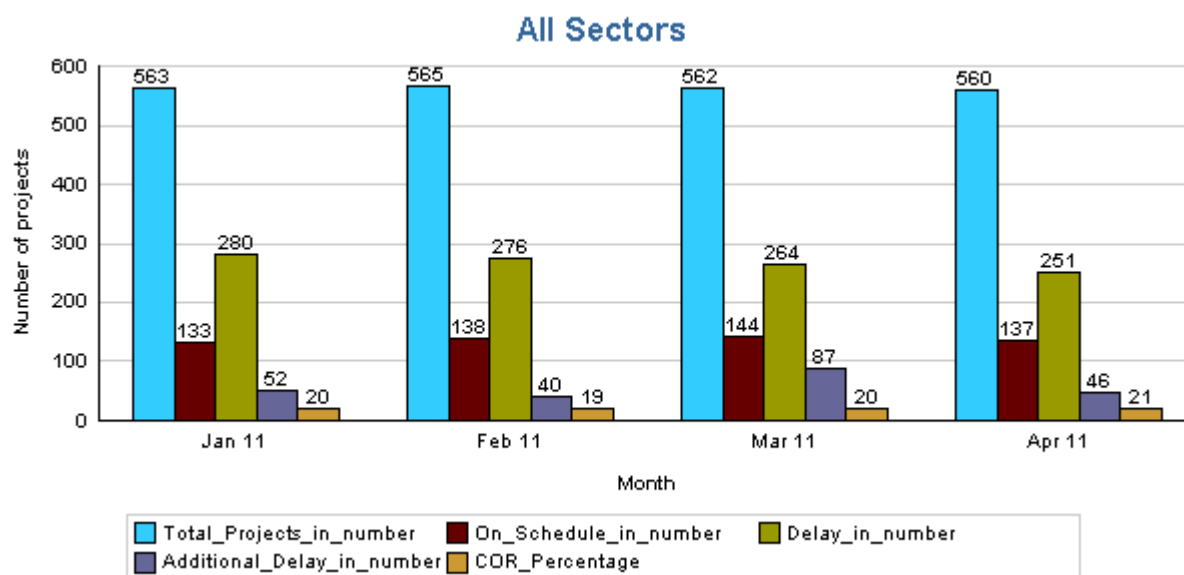


All Sectors Break-up of 251 Delayed projects in April 2011

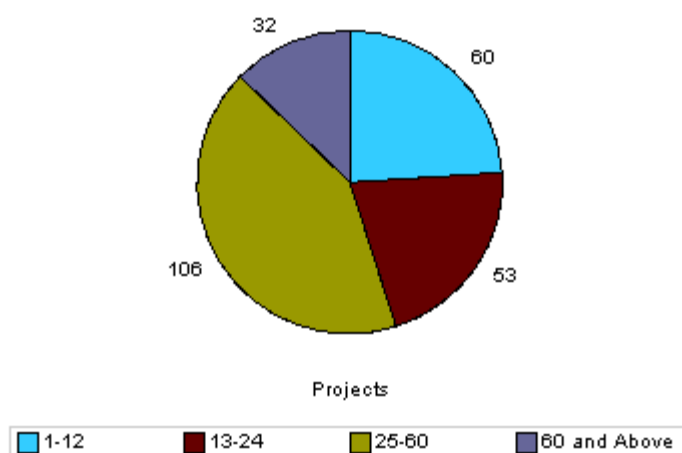

Trend and Graphical Analysis Telecommunications Sector

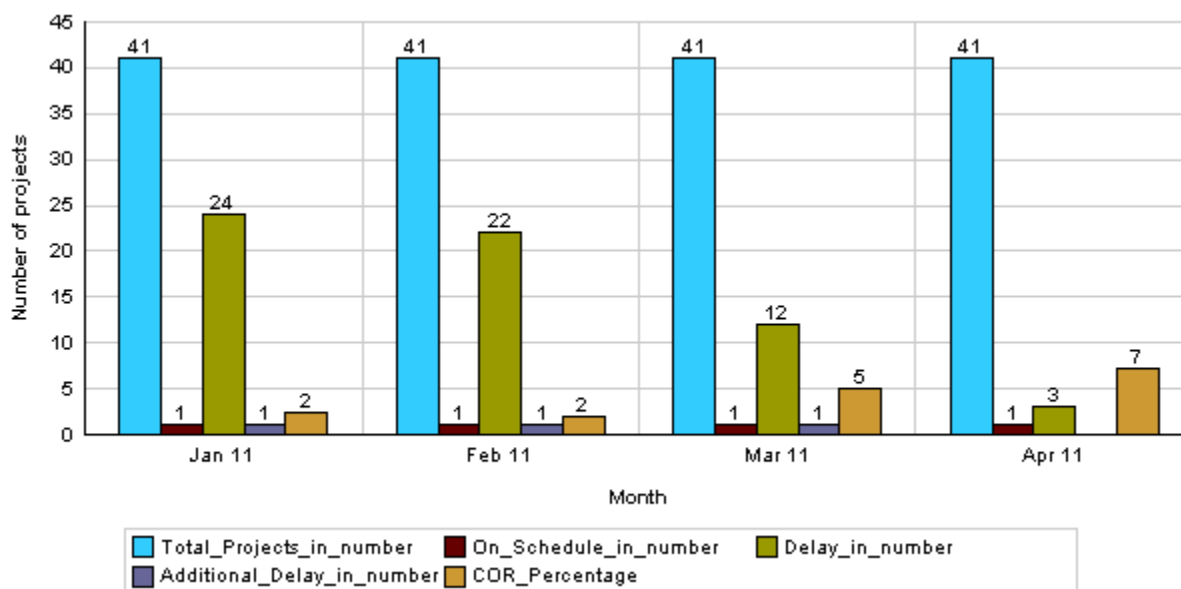


Telecommunications Sector Break-up of 3 Delayed projects in April 2011

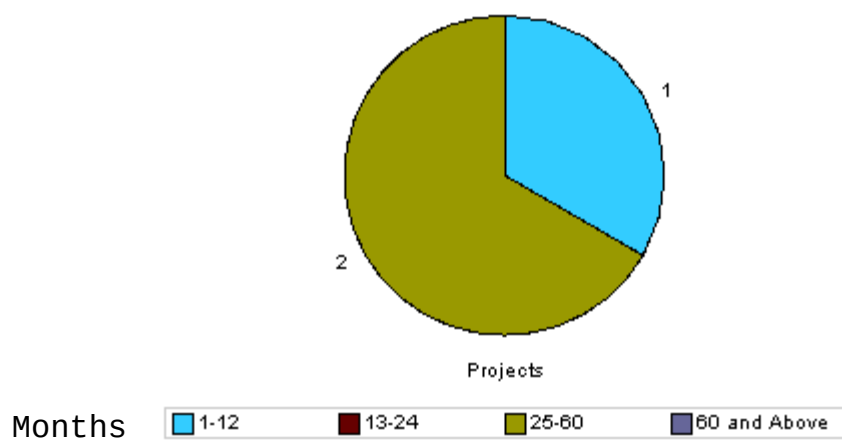


Trend and Graphical Analysis


Steel Sector

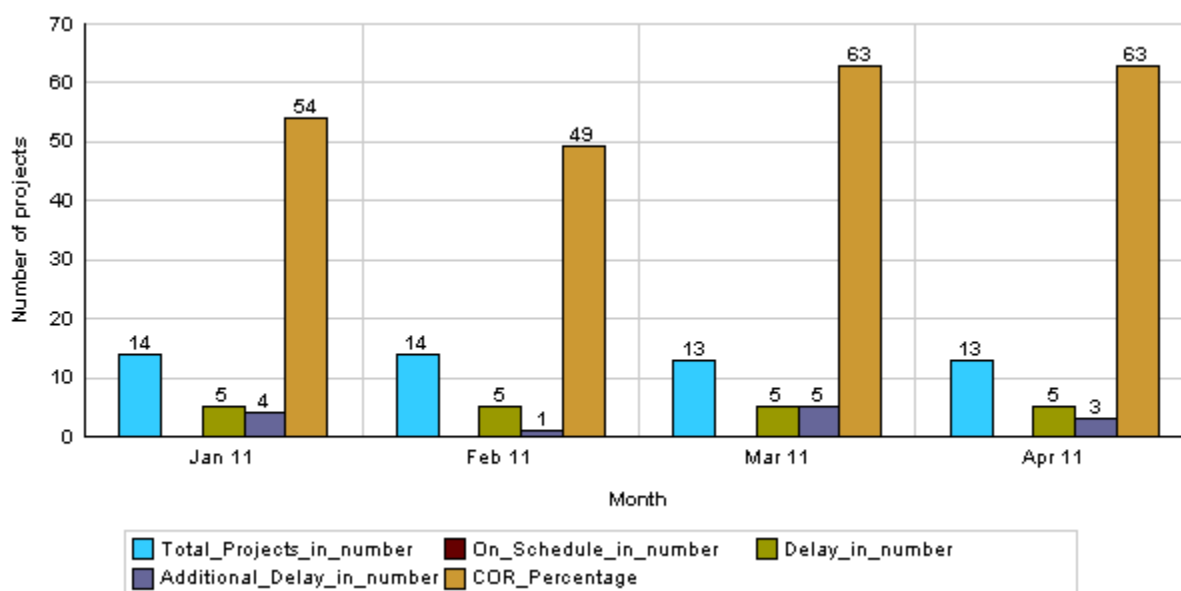


Steel Sector Break-up of 5 Delayed projects in April 2011

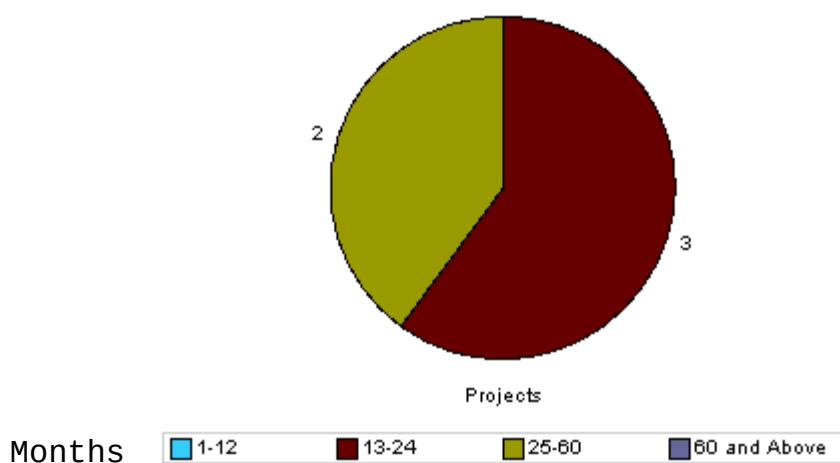


Trend and Graphical Analysis Shipping and Ports Sector

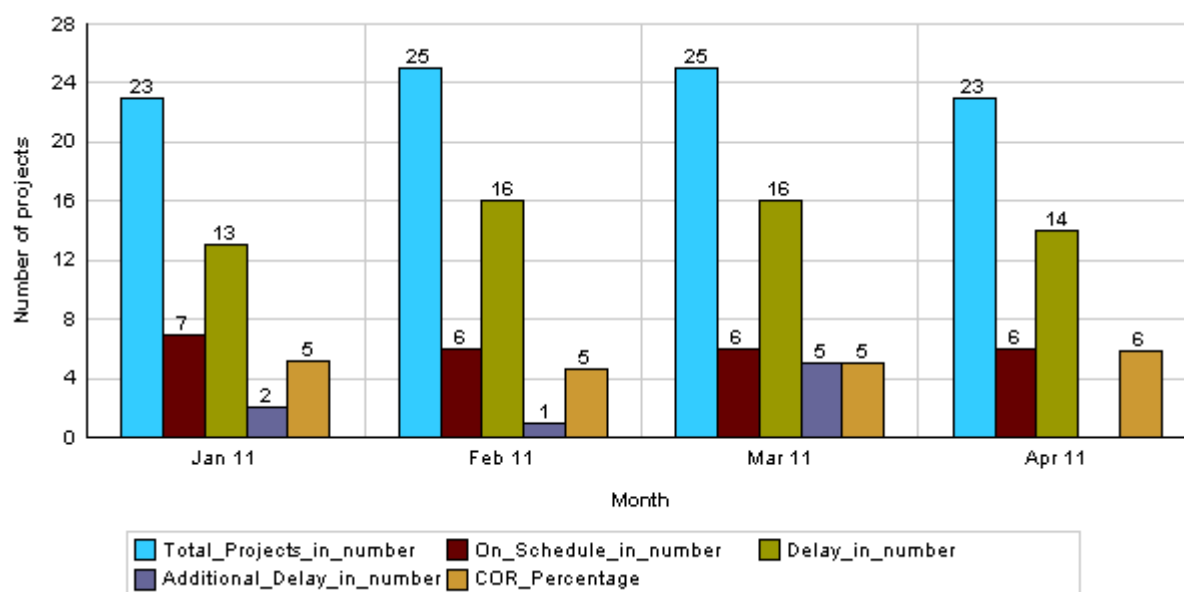


Sector Break-up of 14 Delayed projects in April 2011

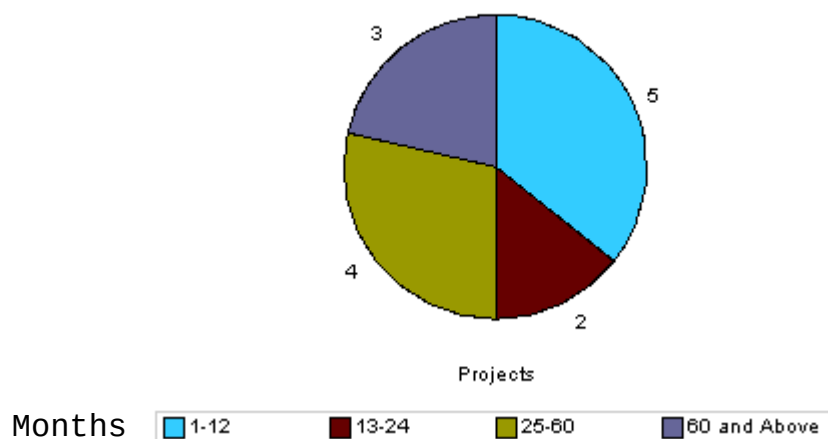

Trend and Graphical Analysis Road Transport and Highways Sector

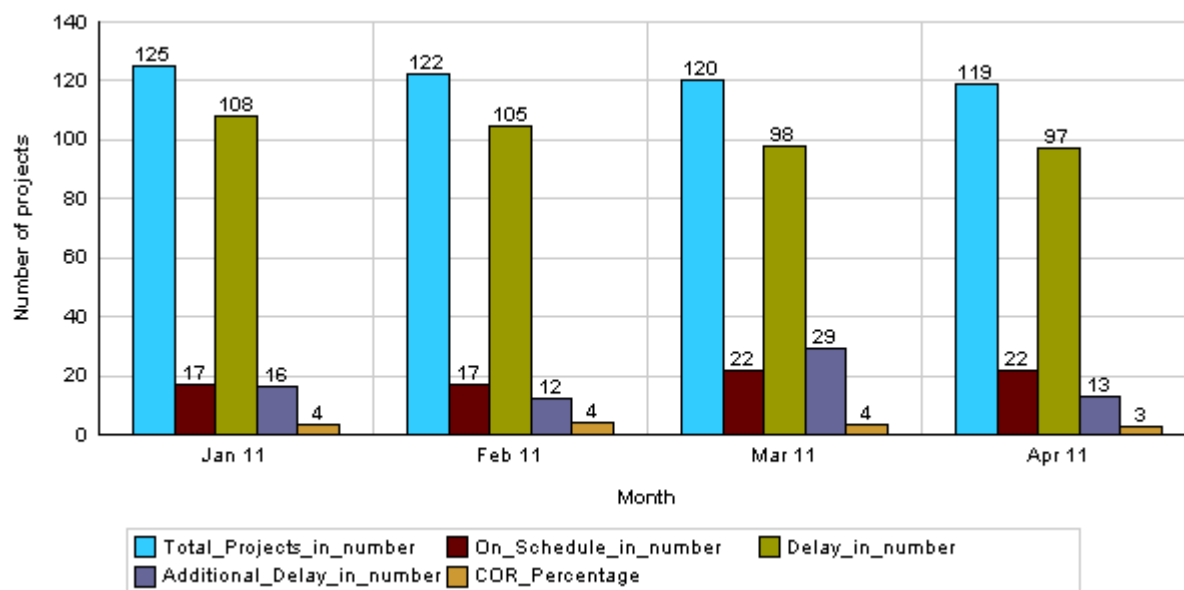


Sector Break-up of 97 Delayed projects in April 2011

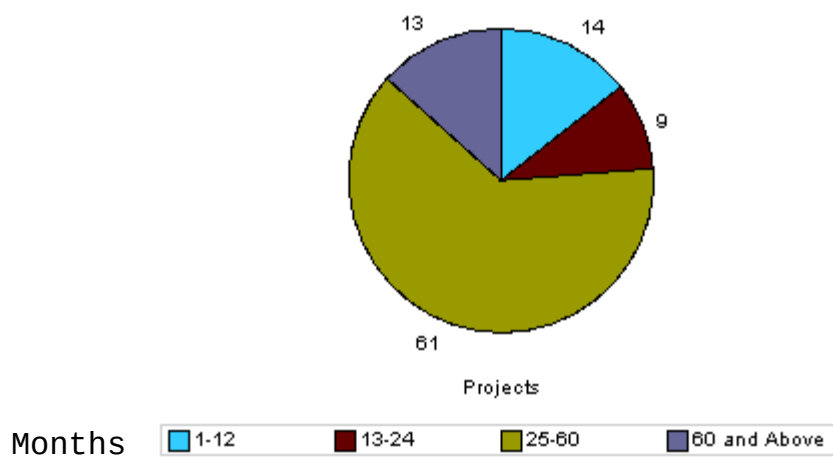


Trend and Graphical Analysis

Railways Sector

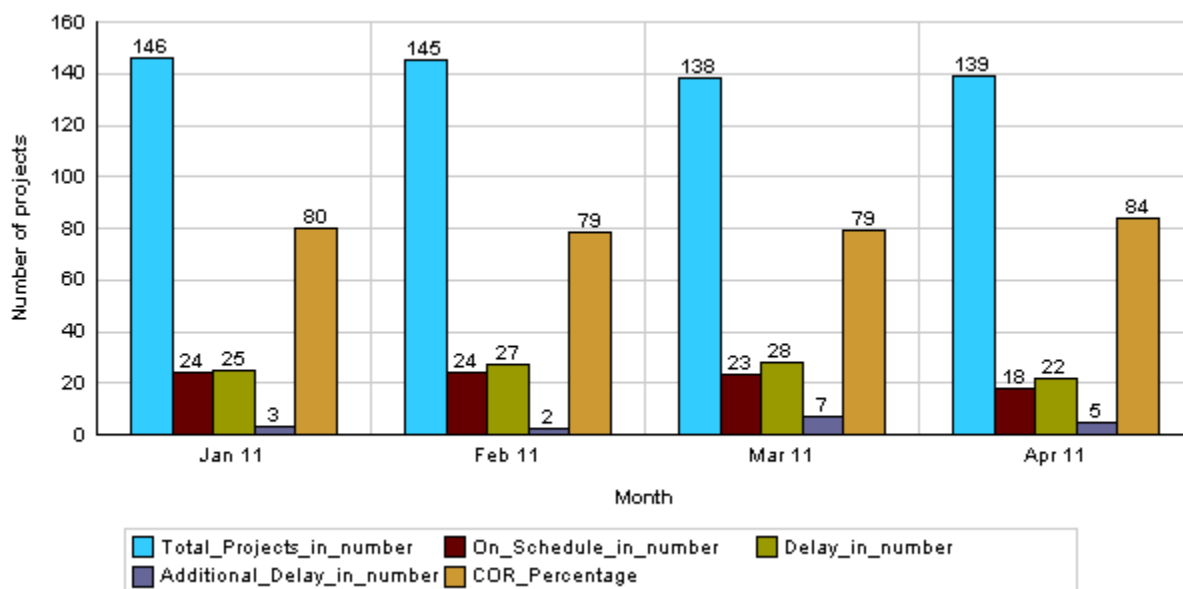


Railways Sector Sector Break-up of 22 Delayed projects in April 2011

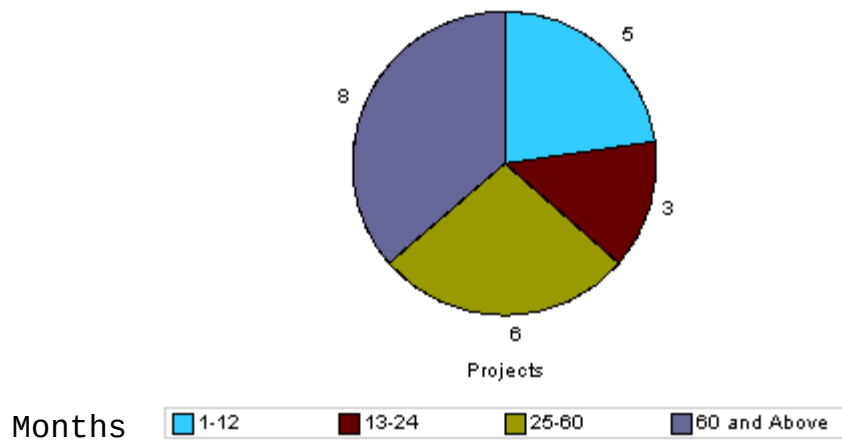


Trend and Graphical Analysis

Power Sector

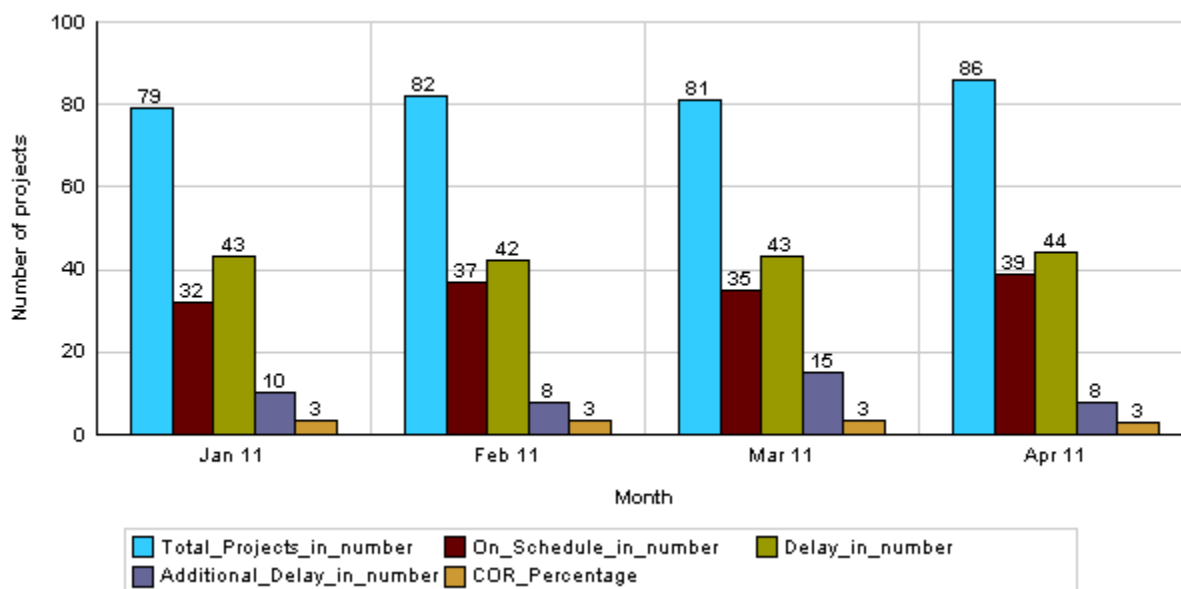


Power Sector Sector Break-up of 44 Delayed projects in April 2011

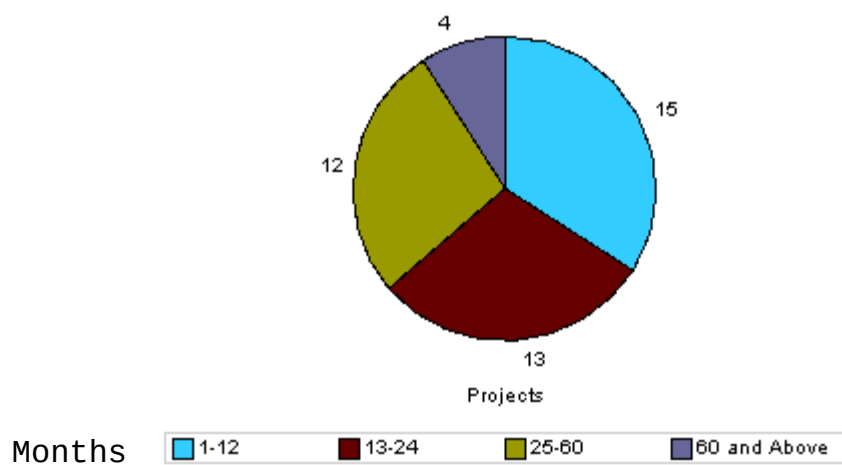


Trend and Graphical Analysis

Petroleum Sector

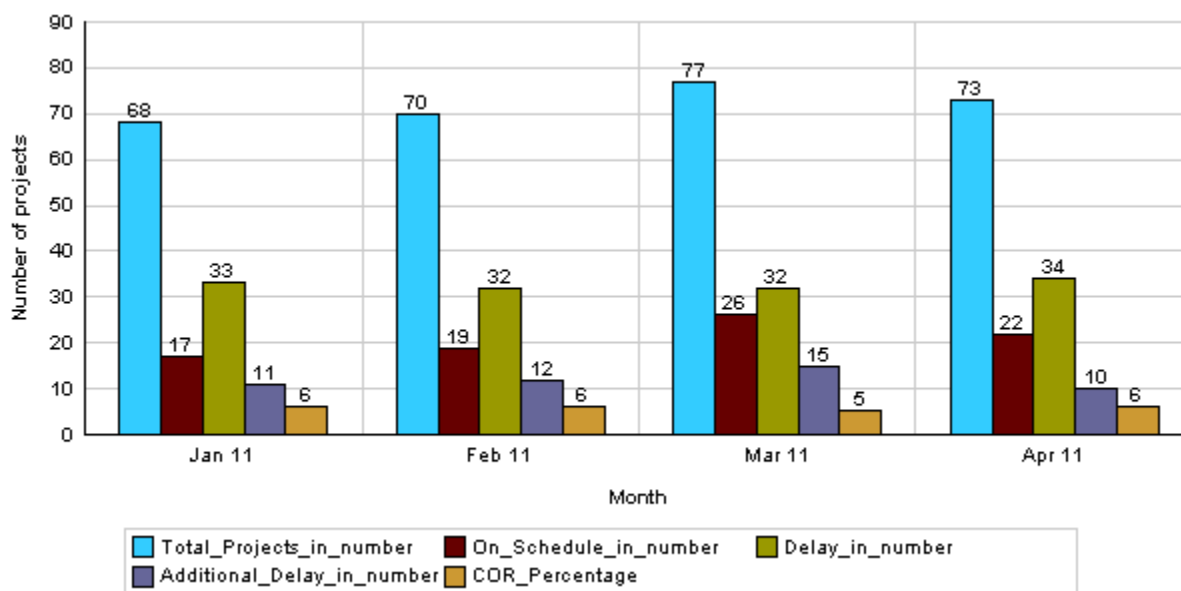

Petroleum Sector Sector Break-up of 34 Delayed projects in April 2011

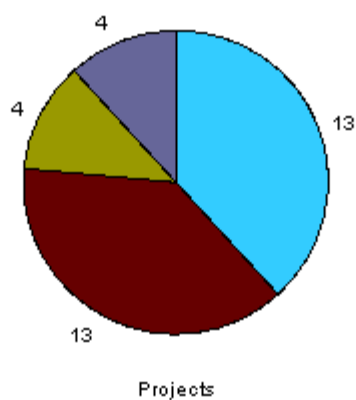


Months




Trend and Graphical Analysis

Coal Sector

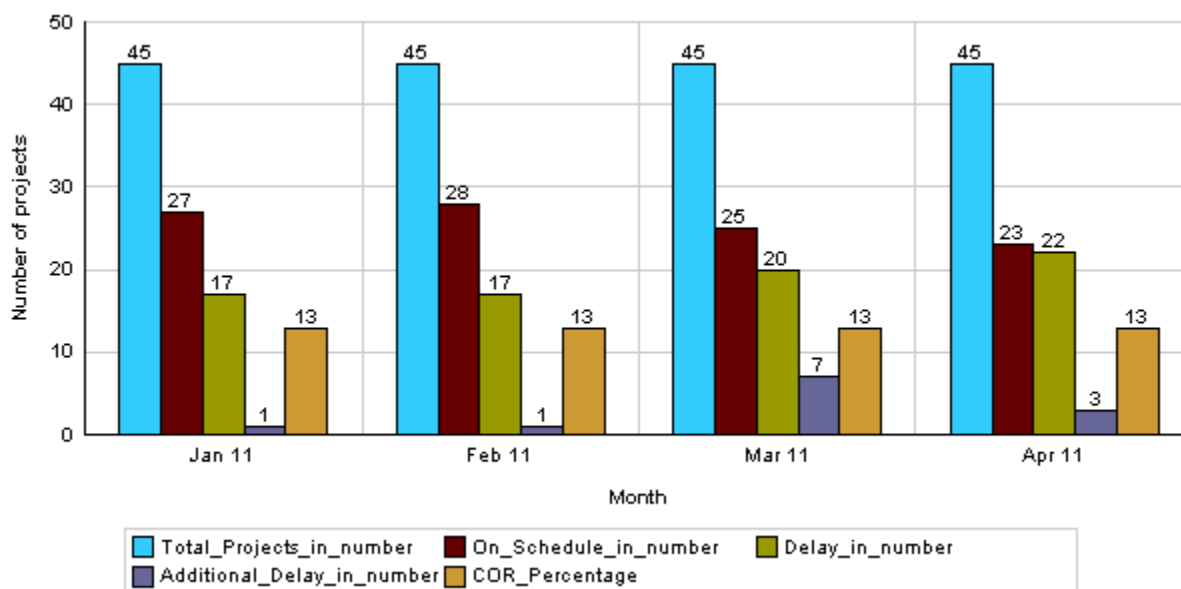


Coal Sector Sector Break-up of 22 Delayed projects in April 2011

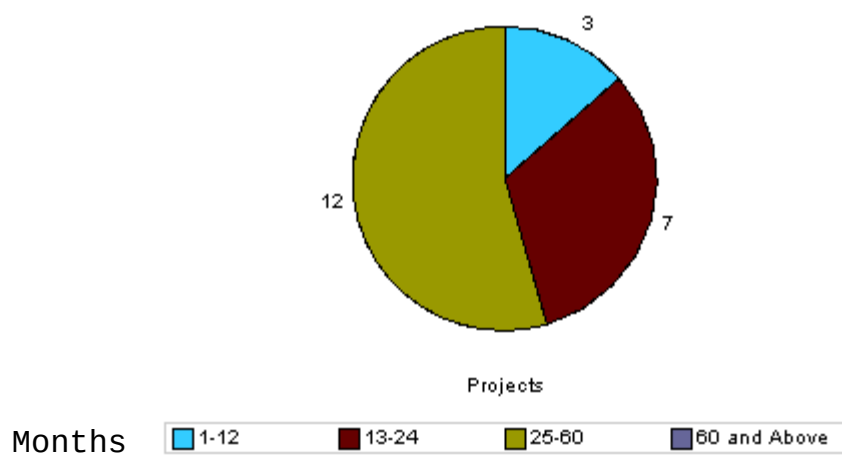


Trend and Graphical Analysis

Civil Aviation Sector

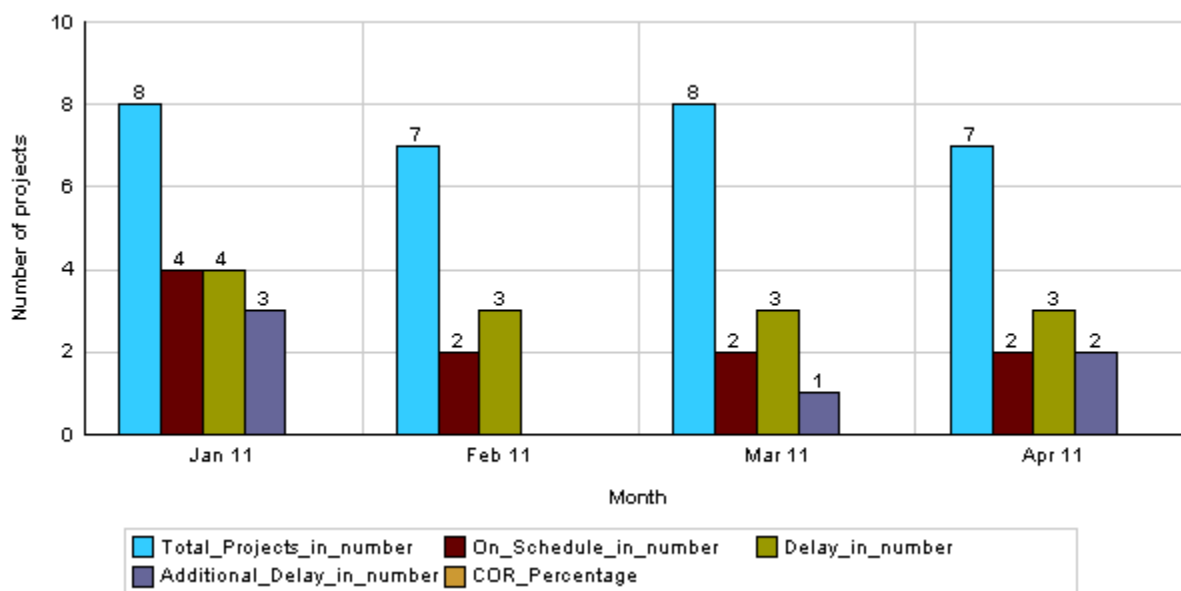


Civil Aviation Sector Sector Break-up of 3 Delayed projects in April 2011

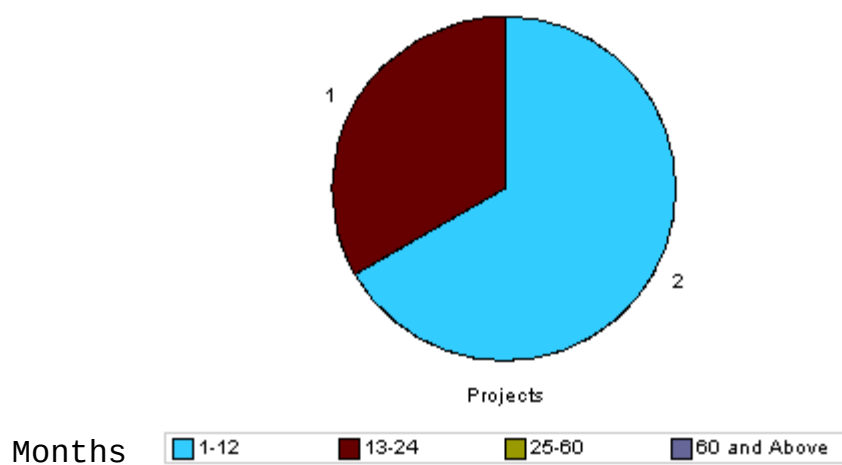


Trend and Graphical Analysis

Atomic Energy Sector

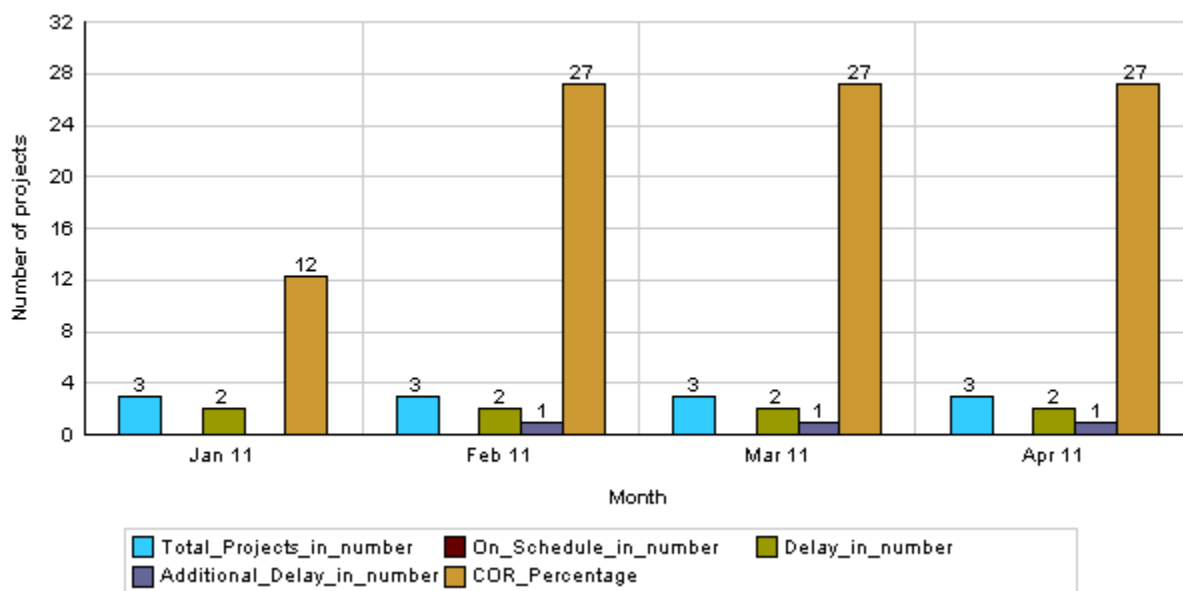

Atomic Energy Sector Sector Break-up of 2 Delayed projects in April 2011

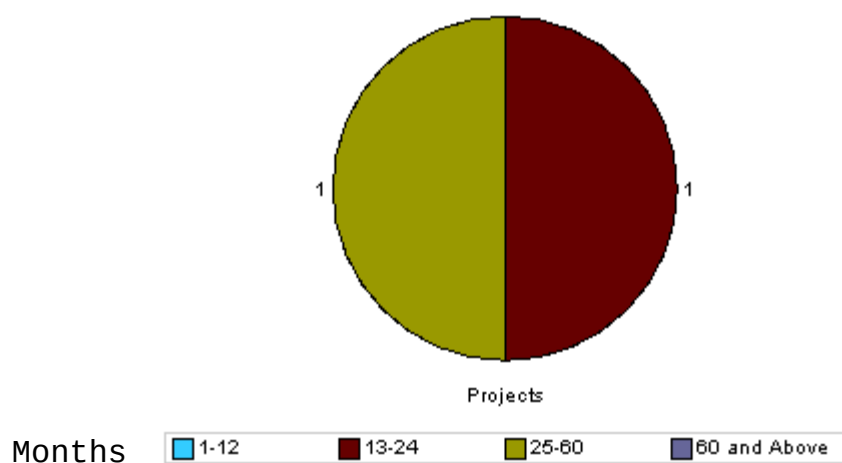

Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)		
		Original	Latest	Anticipated
Atomic Energy	3	17,769.29	17,769.29	22,607.29
Civil Aviation	7	4,826.48	4,826.48	4,826.48
Coal	45	25,509.15	28,789.49	28,789.48
Fertilisers	6	5,317.41	5,317.41	5,317.41
Mines	1	4,091.51	4,401.76	4,401.76
Steel	13	39,927.85	55,138.50	65,040.88
Petroleum	73	157,868.41	169,601.11	167,284.98
Power	86	178,558.19	179,513.81	184,085.59
Railways	139	66,775.98	84,750.06	123,021.21
Road Transport & Highways	119	52,920.82	52,920.82	54,384.23
Shipping & Ports	23	14,464.19	15,142.21	15,317.65
Telecommunications	41	20,025.99	19,979.50	21,450.84
Urban Development	3	15,185.18	15,173.44	30,684.66
Water Resources	1	542.90	542.90	1,187.00
Grand total	560	603,783.35	653,866.78	728,399.46

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Atomic Energy</u>									
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00 -	5,677.00	2,976.38	09/2010 -	01/2012	16(O)	8/80
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00 -	15,824.00	13,781.00	12/2008 -	03/2012	39(O)	61/119
3	URANIUM ORE MINE & PROCESSING PLANT AT TUMMALAPALL - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29 -	1,106.29	965.76	- 04/2011	04/2012	12(R3)	0/1
Total			17,769.29 -	22,607.29	17,723.14				69/200
<u>Civil Aviation</u>									
4	CONSTRUCTION OF RCC/PRE STRESSD CONCRETE BRIDGE K3 - [N04000068]AAI,Tamil Nadu	06/2009	213.35 -	213.35	60.89	09/2010 -	03/2011	6(O)	0/0
5	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	1,942.51	1,133.06	05/2011 -	08/2011	3(O)	0/0
6	D/O KAMARAJ DOMESTIC TER-PH-II & EXP. ANNA INT. TE(K1) - [N04000038]AAI,Tamil Nadu	08/2008	1,273.00 -	1,273.00	797.20	01/2011 -	10/2011	9(O)	0/0
7	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	204.73 -	204.73	32.50	05/2012 -	05/2012	0(O)	0/0
8	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	264.29 -	264.29	136.56	01/2011 -	06/2012	17(O)	0/0
9	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	393.60 -	393.60	160.29	06/2013 -	06/2013	0(O)	0/0
10	D/O OF TERMINAL BLDG. AND PAVEMENT WORKS AT CHENNA - [N04000040]AAI,Tamil Nadu	01/2008	535.00 -	535.00	143.97	06/2010 -	-	-	0/0
Total			4,826.48 -	4,826.48	2,464.47				0/0
<u>Coal</u>									
11	BARSINGSAR TPS (2X125MW) (NLC) - [060100089]NLC,Rajasthan	12/2004	1,114.18 1,626.09	1,626.09	1,587.80	06/2009 -	06/2011	24(O)	59/26
12	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 2,453.57	2,453.57	2,171.59	06/2009 -	03/2012	33(O)	60/24
13	KULDA OCP (MAHANADI COALFIELDS LTD.) - [060100092]MCL,Orissa	01/2005	302.96 -	302.96	76.47	03/2010 03/2012	03/2012	0(R3)	0/4
14	NIGAH OCP EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40 -	259.40	1.49	03/2012 -	03/2012	0(O)	0/1
15	BALRAM OCP EXTENSION - [N06000044]MCL,Orissa	12/2007	172.08 -	172.08	-	03/2009 03/2010	03/2012	24(R3)	0/2
16	ANANTA OCP EXPANSION PH-III - [N06000067]MCL,Orissa	08/2008	207.28 -	207.28	60.77	03/2012 -	03/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
17	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97 -	418.97	71.74	03/2012 -	03/2012	0(O)	28/27
18	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19 -	181.19	0.91	03/2012 -	03/2012	0(O)	7/34
19	TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC,Tamil Nadu	05/2008	4,909.54 4,909.54	4,909.54	1,642.72	08/2012 -	10/2012	2(O)	0/3
20	ASHOK EXPN.OCP -CCL (5 MTY) - [060100096]CCL,Jharkhandd	04/2006	471.66 341.63	341.63	98.32	03/2011 03/2013	03/2013	0(R3)	0/2
21	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Madhya pradesh	05/2006	789.88 741.56	741.56	137.37	03/2010 -	03/2013	36(O)	0/2
22	KUSMUNDA EXPN.OCP(SECL)(10MTY) - [N06000008]SECL,Chhatisgarh	06/2006	737.65 1,188.31	1,188.31	576.97	03/2013 -	03/2013	0(O)	0/3
23	KANIHA OCP - [N06000035]MCL,Multi State	12/2007	457.77 -	457.77	69.13	03/2013 -	03/2013	0(O)	0/2
24	HINGULA OC-II EXP. PH-II (15 MTY) - [N06000068]MCL,Orissa	11/2008	479.53 -	479.53	205.76	03/2013 -	03/2013	0(O)	0/2
25	Purnadih OCP - [N06000085]CCL,Jharkhandd	07/2008	210.98 -	210.98	19.88	03/2013 -	03/2013	0(O)	0/2
26	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	09/2006	212.34 779.26	779.26	154.70	03/2013 09/2012	06/2013	9(R3)	2/22
27	GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093]SECL,Chhatisgarh	07/2005	1,667.55 2,675.67	2,675.67	1,089.83	03/2010 03/2014	03/2014	0(R3)	3/2
28	DIPKA EXPANSION OCP (SECL) (20 MTY) - [060100094]SECL,Chhatisgarh	07/2005	1,268.53 1,943.66	1,943.66	1,019.45	03/2010 03/2014	03/2014	0(R3)	2/3
29	BINA EXTN. PROJ - [N06000019]NCL,Multi State	11/2006	168.97 -	168.97	137.37	03/2014 -	03/2014	0(O)	1/2
30	CHURCHA UG - [N06000046]SECL,Chhatisgarh	06/2008	462.35 -	462.35	255.90	03/2014 -	03/2014	0(O)	0/2
31	RAJMAHAL OC EXP. - [N06000056]ECL,Multi State	02/2006	50.08 153.82	153.82	17.12	03/2011 -	03/2014	36(O)	0/3
32	PENGANGA OC - [N06000066]WCL,Andhra Pradesh	10/2008	339.77 -	339.77	-	03/2014 -	03/2014	0(O)	1/2
33	KARTALI (EAST) OC - [N06000076]SECL,Chhatisgarh	07/2008	178.44 -	178.44	-	03/2014 -	03/2014	0(O)	0/1
34	MANIKPUR OC EXPANTION - [N06000081]SECL,Chhatisgarh	11/2009	321.50 -	321.50	213.92	03/2014 -	03/2014	0(O)	0/1
35	Churi Benti UG - [N06000083]CCL,Jharkhandd	06/2007	163.51 -	163.51	33.44	03/2011 03/2012	03/2014	24(R3)	0/2
36	North Urimari OCP - [N06000084]CCL,Jharkhandd	12/2007	179.87 -	179.87	62.99	03/2012 -	03/2014	24(O)	0/2
37	Tapin OCP - [N06000086]CCL,Jharkhandd	08/2008	264.68 -	264.68	59.68	03/2012 03/2013	03/2014	12(R3)	0/2
38	KARMA OCP - [N06000088]CCL,Jharkhandd	06/2009	162.46 -	162.46	-	03/2014 -	03/2014	0(O)	0/0
39	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04 437.34	437.34	137.91	03/2012 03/2015	03/2015	0(R3)	0/2
40	JHANJRA LONGWAL UG PHASE II - [N06000020]ECL,West Bengal	11/2006	287.18 -	287.17	-	03/2011 03/2015	03/2015	0(R3)	1/5

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
41	GOPAL PRASAD OCP - [N06000042]MCL,Orissa	02/2008	395.87	395.87	23.97	03/2013 03/2015	03/2015	0(R3)	0/3
42	PELMA OC - [N06000045]SECL,Chhatisgarh	07/2008	448.32	448.32	-	03/2015	03/2015	0(O)	0/1
43	KAKATIYA LAONGWALL - [N06000048]SCCL,Multi State	12/2008	453.63	453.63	61.32	12/2012	03/2015	27(O)	11/44
44	Batura OC - [N06000049]SECL,Madhya pradesh	09/2008	203.82	203.82	-	03/2015	03/2015	0(O)	0/1
45	JAGANNATHPOR OC - [N06000075]SECL,Chhatisgarh	09/2008	152.43	152.43	-	03/2015	03/2015	0(O)	0/1
46	Kistaram OCP - [N06000089]SCCL,Andhra Pradesh	11/2010	242.29	242.29	-	03/2015	03/2015	0(O)	0/28
47	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]NCL,Madhya pradesh	05/2006	1,352.04 1,143.54	1,143.54	66.62	03/2014 03/2016	03/2016	0(R3)	1/2
48	MAGADH OC (CCL) - [N06000015]CCL,Jharkhandd	07/2006	469.78 706.40	706.40	16.13	07/2012 03/2014	03/2016	24(R3)	0/2
49	TALABIRA OCP - [N06000043]MCL,Orissa	03/2008	447.72	447.72	35.20	03/2015 03/2016	03/2016	0(R3)	0/2
50	AMLAI OC EXPANSION SECTOR 'B' (1.50 MTY) - [N06000082]SECL,Chhatisgarh	11/2009	198.59	198.59	108.57	03/2016	03/2016	0(O)	0/1
51	Rajrappa RCE OCP - [N06000087]CCL,Jharkhandd	12/2009	510.85	510.85	284.97	03/2016	03/2016	0(O)	0/2
52	BHUBANESWARI OCP - [N06000034]MCL,Orissa	12/2007	490.10	490.10	75.16	03/2017	03/2017	0(O)	0/1
53	RKP OCP PHASE-I - [N06000079]SCCL,Uttaranchal	03/2010	209.78	209.78	15.88	03/2015	03/2018	36(O)	4/31
54	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03	249.03	38.37	03/2012	03/2012	0(O)	13/42
55	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	03/2013	467.78	467.78	11.86	03/2013	03/2013	0(O)	0/83
	Total		25,509.15	28,789.48	10,641.28				193/429
Fertilisers									
56	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00	325.00	-	07/2011	07/2011	0(O)	0/0
57	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00	438.00	-	07/2011	07/2011	0(O)	0/0
58	THAL AMMONIA REVAMP PROJECT - [N08000003]RCF,Haryana	01/2009	488.75	488.75	68.81	- 11/2011	11/2011	0(R3)	2/22
59	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJE - [N08000004]NFL,Haryana	01/2010	1,292.84	1,292.84	120.91	01/2013	01/2013	0(O)	0/5
60	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJ - [N08000005]NFL,Punjab	01/2010	1,294.19	1,294.19	112.31	01/2013	01/2013	0(O)	0/5

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
61	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,Punjab	01/2010	1,478.63	1,478.63	113.16	12/2012	01/2013	1(O)	0/8
	Total		5,317.41	5,317.41	415.19				2/40
			-						
	<u>Mines</u>								
62	SECOND PHASE EXPANSION OF CAPTIVE ALUMINIUM,SMELTER AND POWE - [100100054]NALCO,Orissa	10/2004	4,091.51	4,401.76	3,648.20	12/2008	05/2011	4(R3)	117/110
	Total		4,091.51	4,401.76	3,648.20				117/110
			-						
	<u>Steel</u>								
63	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]SAIL,Chhatisgarh	07/2007	111.28	232.93	135.00	-	07/2011	-	0/1
			232.93			-			
64	REBUILDING OF COKE OVEN BATTERY NO-6 (BSP) - [N12000054]SAIL,Jharkhandd	07/2008	172.78	172.78	127.00	01/2010	07/2011	18(O)	0/1
			-			-			
65	Rebuilding of coke oven battery No.1 & 2 (Bokaro S - [N12000033]SAIL,Jharkhandd	10/2007	500.90	500.90	174.51	04/2010	09/2011	17(O)	0/2
			-			-			
66	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,	07/2007	230.00	343.58	219.75	-	09/2011	-	0/3
			-			-			
67	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,	07/2007	260.00	350.00	214.80	-	09/2011	-	0/2
			-			-			
68	Deve. of Bailadila Iron Ore Deposit-II(B)(NMDC) - [N12000018]NMDC,Chhatisgarh	01/2003	295.89	607.17	264.84	-	10/2011	-	2/21
			-			-			
69	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00	14,443.00	10,747.99	09/2010	12/2011	0(R3)	0/6
			-			12/2011			
70	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhandd	01/2008	3,316.00	6,325.00	1,904.73	-	12/2011	0(R3)	0/7
			6,325.00			12/2011			
71	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00	12,291.00	8,276.00	10/2009	03/2012	29(O)	7/58
			-			-			
72	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,	05/2008	480.00	480.84	83.29	-	05/2012	0(R3)	1/2
			-						
73	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,	08/2007	108.00	216.68	35.39	-	10/2012	0(R3)	0/4
			-			10/2012			
74	EXPENSION OF ROURKELA STEEL PLANT - [N12000056]SAIL,Orissa	09/2008	6,133.00	11,812.00	-	02/2011	03/2013	25(O)	0/0
			-			-			
75	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	5,185.00	17,265.00	2,500.36	-	03/2013	0(R3)	0/8
			17,265.00			03/2013			
	Total		39,927.85	65,040.88	24,683.66				10/115
			-						
	<u>Petroleum</u>								

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
76	CAPACITY EXP. CUM MODERNISATION PH-II - [N16000080]BPCL,Kerala	09/2009	2,591.80 3,941.41	3,941.41	3,249.54	12/2009 -	12/2010	12(O)	0/0
77	C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC) - [160100168]ONGC,Gujarat	12/2003	900.92 1,493.49	976.08	770.48	05/2008 07/2010	04/2011	9(R3)	0/2
78	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,218.01	2,218.01	1,237.61	04/2006 05/2011	05/2011	0(R3)	0/0
79	MNW-NF BRIDGE PROJECT - [N16000045]ONGC,Maharashtra	05/2008	175.21 -	175.21	58.26	03/2009 -	05/2011	26(O)	0/0
80	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	755.76	398.59	03/2011 05/2011	05/2011	0(R3)	0/0
81	Pipeline Replacement project-2 - [N16000111]ONGC,Multi State	12/2007	2,553.28 3,796.21	3,796.21	3,579.42	05/2011 -	05/2011	0(O)	0/0
82	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON - [N16000009]BRPL,Assam	06/2006	1,431.91 1,646.39	1,690.13	1,573.04	09/2009 -	06/2011	21(O)	0/0
83	HEERA RECONSTRUCTION - [N16000062]ONGC,Maharashtra	05/2008	706.70 -	706.70	567.05	04/2010 -	06/2011	14(O)	0/0
84	NEELAM RECONSTRUCTION - [N16000063]ONGC,Maharashtra	05/2008	305.08 -	305.08	220.26	04/2011 -	06/2011	2(O)	0/0
85	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- - [N16000070]GAIL,Multi State	07/2009	238.68 196.25	200.00	76.55	- 06/2011	06/2011	0(R3)	1/8
86	REFRIGERATED LPG STORAGE AT JNPT - [N16000083]BPCL,Maharashtra	06/2008	304.40 -	304.40	227.20	12/2010 -	06/2011	6(O)	0/0
87	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli - [N16000102]HPCL,Bihar	06/2009	613.54 -	727.88	164.16	12/2010 -	06/2011	6(O)	0/0
88	MSQ QUALITY UP GRADATION PROJECT AT BONGAIGAON REF - [N16000040]IOCL,Assam	04/2008	293.60 -	294.00	218.62	12/2009 -	07/2011	19(O)	0/0
89	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 -	299.00	190.00	12/2010 02/2011	08/2011	6(R3)	0/0
90	DAHEJ-VIJAYPUR PIPE LINE PROJECT(PHASE-II) - [N16000052]GAIL,Multi State	11/2007	4,403.26 4,403.26	2,500.00	2,094.64	10/2011 09/2011	09/2011	0(R3)	0/2
91	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 -	756.00	623.23	12/2011 -	09/2011	-3(O)	0/0
92	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 -	3,284.00	-	09/2011 -	09/2011	0(O)	0/0
93	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT - [N16000024]ONGC,Maharashtra	09/2006	2,305.30 700.00	3,005.30	2,416.96	06/2010 06/2010	10/2011	16(R3)	0/0
94	Construction of tanks and blending facility at vadinar - [N16000115]IOCL,Gujarat	02/2009	267.00 -	267.00	159.28	09/2012 -	10/2011	-11(O)	0/0
95	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 -	3,195.16	2,520.91	12/2008 12/2008	11/2011	35(R3)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
96	BAWANA NANGAL PIPE LINE PROJECT - [N16000050]GAIL,Multi State	11/2007	1,816.07 1,816.07	1,400.00	777.10	- 12/2011	12/2011	0(R3)	0/1
97	COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I - [N16000053]GAIL, Madhya pradesh	11/2007	1,512.00 1,434.00	982.00	831.88	04/2011 12/2011	12/2011	0(R3)	0/3
98	COMPRESSOR STATIONS (KAILARAS & CHAINSA) - [N16000054]GAIL, Multi State	11/2007	1,167.00 1,167.00	810.00	350.39	04/2011 12/2011	12/2011	0(R3)	0/2
99	BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]IOCL, Gujarat	02/2009	250.00 349.00	250.00	164.46	03/2013 -	12/2011	-15(O)	0/0
100	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC, Multi State	06/2007	736.65 -	736.65	210.29	09/2011 -	12/2011	3(O)	0/0
101	EURO-IV DHD - [N16000109]CPCL, Tamil Nadu	09/2008	2,615.69 -	2,615.69	1,510.82	05/2011 -	12/2011	7(O)	0/116
102	HYDROCRACKER REVAMP & SETTING UP A NEW CCR AT MUMB - [N16000081]BPCL, Maharashtra	02/2008	825.00 -	825.00	103.89	- 12/2011	01/2012	1(R3)	0/203
103	MRPL Phase-III Expansion - [N16000114]Mangalore Refin, Karnataka	08/2008	12,412.00 -	12,160.00	5,578.00	01/2012 -	01/2012	0(O)	0/0
104	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC, Maharashtra	01/2007	740.02 -	740.02	412.78	03/2010 03/2012	03/2012	0(R1)	0/0
105	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL, Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	432.33	09/2011 03/2012	03/2012	0(R3)	0/0
106	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL, Multi State	12/2009	463.32 -	340.00	62.22	06/2011 03/2012	03/2012	0(R3)	3/9
107	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC, Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,093.65	09/2010 03/2012	04/2012	1(R3)	0/0
108	Assam gas Cracker project - [N16000106]BCPL, Assam	04/2006	5,460.61 -	5,460.61	2,206.65	- -	04/2012	-	0/30
109	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC, Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	2,912.73	05/2010 05/2012	05/2012	0(R3)	0/0
110	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC, Maharashtra	05/2008	333.40 837.54	656.51	3.52	05/2010 04/2012	05/2012	1(R3)	0/0
111	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC, Maharashtra	06/2007	1,436.21 1,456.96	1,456.96	52.56	07/2010 05/2012	05/2012	0(R3)	0/0
112	CDU/VDU-II - [N16000110]CPCL, Tamil Nadu	03/2010	333.99 -	333.99	29.43	05/2012 08/2010	05/2012	21(R3)	5/36
113	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC, Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	1,113.85	08/2010 03/2012	06/2012	3(R3)	0/0
114	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC, Multi State	01/2010	2,163.64 -	2,163.64	491.77	06/2012 -	06/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
115	INTEGRATED OFFSHORE CRUDE OIL HANDLING FACILITIES - [N16000090]IOCL,Orissa	12/2009	1,492.33	1,492.33	614.18	-	06/2012	-	6/9
116	Wind Power Project - [N16000119]ONGC,Gujarat	07/2010	1,106.00	1,106.00	-	06/2012	06/2012	0(O)	0/0
117	ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11	370.11	46.00	04/2011	07/2012	15(O)	0/0
118	BNPL SPURLINE (UTTRANCHAL & PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92	400.00	23.64	06/2011 07/2012	07/2012	0(R3)	7/9
119	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78	1,803.78	180.13	07/2012	07/2012	0(O)	0/0
120	DHABOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State	06/2009	4,543.43 4,508.38	2,500.00	417.04	03/2012 08/2012	08/2012	0(R3)	11/10
121	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	253.66	45.06	08/2012	08/2012	0(O)	0/0
122	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39	7,133.39	1,973.46	09/2012	09/2012	0(O)	0/0
123	PARADIP-RAIPUR-SAMBALPUR-RANCHI PIPELINE - [N16000088]IOCL,Multi State	08/2009	1,793.00	1,400.00	286.94	-	09/2012	-	0/15
124	Construction of six Effluent Treatment Plants (ETP) - [N16000099]ONGC,Gujarat	03/2009	234.78 234.78	234.78	-	09/2012	09/2012	0(O)	0/0
125	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26	302.26	15.78	09/2012	09/2012	0(O)	0/0
126	PARADIP REFINERY PROJECT - [N16000058]IOCL,Orissa	02/2009	29,777.00	29,777.00	6,657.79	-	11/2012	-	107/103
127	KOCHI-KANJIRKOD BANGALORE-MANGALORE PIPELINE PROJECT PHASE-I - [N16000071]GAIL,Multi State	06/2009	348.00 348.00	260.00	107.77	03/2012 12/2012	12/2012	0(R3)	6/12
128	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35	890.37	49.86	12/2011	01/2013	13(O)	0/0
129	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00	1,000.00	8.95	-	01/2013	-	11/18
130	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44	410.44	-	01/2013	01/2013	0(O)	0/0
131	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]IOCL,Haryana	11/2009	341.50	341.50	3.81	-	02/2013	-	11/42
132	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	218.08	03/2006 03/2013	03/2013	0(R3)	6/6
133	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03	8,813.41	6,641.54	05/2010 03/2013	03/2013	0(R3)	0/0
134	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15	2,378.86	281.62	03/2013	03/2013	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
135	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64	723.64	-	03/2013	03/2013	0(O)	0/0
136	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03	3,241.03	-	03/2013	03/2013	0(O)	0/0
137	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11	372.11	-	03/2013	03/2013	0(O)	0/0
138	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20	331.20	-	08/2013	03/2013	-5(O)	0/0
139	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00	1,584.00	1.69	-	08/2013	-	0/0
140	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00	2,523.00	-	01/2014	01/2014	0(O)	0/0
141	Wax Project - [N16000101]NRL,Assam	08/2010	576.60	576.60	6.48	02/2014	02/2014	0(O)	0/0
142	Petrochemical Complex-II - [N16000112]GAIL,Multi State	08/2010	8,140.00	8,140.00	65.17	02/2014	02/2014	0(O)	0/0
143	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10	663.69	559.61	03/2007 03/2014	03/2014	0(R3)	3/3
144	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10	1,916.10	-	12/2014	12/2014	0(O)	0/0
145	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63	2,189.63	-	12/2014	12/2014	0(O)	0/0
146	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00	3,823.00	-	04/2015	04/2015	0(O)	0/0
147	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09	1,674.11	1,209.98	03/2007 03/2017	03/2017	0(R3)	6/6
148	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07	281.07	3.29	10/2010	-	-	0/0
Total			157,868.41	167,284.98	58,101.99				183/645
Power									
149	TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB G - [N18000037]PGCIL,Haryana	04/2008	290.49	299.08	345.81	04/2010	05/2011	13(O)	0/0
150	KOTESWAR TRANSMISSION SYSTEM (PGCIL) - [180100256]PGCIL,Uttaranchal	06/2006	260.34	241.27	182.44	06/2008	06/2011	36(O)	9/20
151	EAST-WEST TRANSMISSION CORRIDOR STRENGTHENING SCHEME - [260100100]PGCIL,Multi State	06/2006	803.70	803.76	664.23	06/2009	06/2011	24(O)	1/20
152	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96	894.26	676.27	10/2009	06/2011	20(O)	2/20
153	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]PGCIL,Multi State	12/2007	227.52	227.52	131.46	06/2010	06/2011	12(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
154	TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III - [N18000043]PGCIL,Multi State	12/2008	204.07	204.07	107.73	06/2011	06/2011	0(O)	0/0
155	WESTERN REGION STRENGTHENING SCHEME-IX - [N18000050]PGCIL,Multi State	04/2008	230.89	230.89	75.44	01/2011	06/2011	5(O)	0/1
156	TRANSMISSION SYSTEM ASSOCIATED WITH KORBA III GENE - [N18000059]PGCIL,Madhya pradesh	02/2009	276.61	276.61	197.09	06/2011	06/2011	0(O)	0/0
157	TRANSMISSION SYSTEM ASSOCIATED WITH URI-II - [N18000023]PGCIL,J & K	10/2006	238.25	227.03	209.65	05/2011 05/2011	07/2011	2(R3)	0/0
158	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37	297.37	287.91	07/2011	07/2011	0(O)	0/0
159	CHAMERA,STAGE-III (NHPC) - [180100241]NHPC,Himachal Pr.	08/2005	1,405.63	1,405.63	1,585.40	08/2010	08/2011	12(O)	0/0
160	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J & K	08/2006	621.28	621.28	634.74	02/2011	08/2011	6(O)	0/1
161	EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER - [N18000040]PGCIL,Himachal Pr.	09/2007	262.10	262.10	163.60	09/2010	08/2011	11(O)	0/0
162	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) - [180100260]PGCIL,Bihar	12/2005	3,779.46	3,725.13	3,476.02	09/2009	10/2011	25(O)	15/30
163	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J & K	08/2005	1,724.79	1,724.79	1,432.09	11/2009	11/2011	24(O)	0/0
164	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HE - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24	639.52	435.95	01/2010	11/2011	22(O)	0/22
165	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66	509.66	230.37	11/2011	11/2011	0(O)	0/0
166	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69	317.69	49.79	11/2011	11/2011	0(O)	0/0
167	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19	184.19	123.06	11/2011	11/2011	0(O)	0/0
168	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.52	2,304.52	1,431.24	10/2010	12/2011	14(O)	0/0
169	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23	4,978.56	2,875.64	07/2010	12/2011	17(O)	3/20
170	SIMHADRI STPP STAGE -II (NTPC) - [N18000032]NTPC,Andhra Pradesh	08/2007	5,103.39	5,038.53	3,870.00	05/2011	12/2011	7(O)	0/0
171	WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]PGCIL,Multi State	02/2009	664.96	664.96	228.63	02/2012	02/2012	0(O)	0/0
172	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]PGCIL,Multi State	02/2009	409.50	409.50	31.33	02/2012	02/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
173	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	239.43	11/2011 -	02/2012	3(O)	0/0
174	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	115.29	02/2012 -	02/2012	0(O)	0/0
175	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]PGCIL,Rajasthan	02/2009	210.79 -	210.79	143.06	08/2011 -	02/2012	6(O)	0/0
176	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]PGCIL,Multi State	02/2009	353.57 -	353.57	204.48	07/2010 02/2012	02/2012	0(R3)	0/0
177	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10 -	196.10	56.59	07/2011 -	02/2012	7(O)	0/0
178	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32 -	1,347.32	783.35	02/2012 -	02/2012	0(O)	0/0
179	KOTESHWAR HEP(THDC) - [180100184]THDCL,Uttaranchal	04/2000	1,301.56 -	2,398.39	2,348.18	04/2005 -	03/2012	83(O)	2/12
180	SIPAT STPP STAGE - I (NTPC) - [180100229]NTPC,Chhatisgarh	12/2003	8,323.39 -	8,323.39	7,091.00	12/2009 -	03/2012	27(O)	33/56
181	KUDANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29 -	1,946.85	1,706.35	11/2008 -	03/2012	40(O)	25/38
182	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61 -	276.61	64.84	04/2012 -	03/2012	-1(O)	0/0
183	TESSTA LOW DAM - III HYDROELECTRIC POWER PROJECT - [180100222]NHPC,West Bengal	10/2003	768.92 -	768.92	1,301.88	03/2007 -	05/2012	62(O)	1/25
184	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	1,075.12	213.51	05/2012 -	05/2012	0(O)	0/0
185	NIMOO BAZGO HYDROELECTRIC PROJECT (NHPC) - [N18000006]NHPC,J & K	08/2006	611.02 -	611.02	628.64	08/2010 -	06/2012	22(O)	0/0
186	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36 -	1,736.36	268.20	06/2012 -	06/2012	0(O)	0/0
187	IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS - [N18000082]PGCIL,Bihar	02/2010	215.86 -	215.86	100.80	06/2012 -	06/2012	0(O)	0/0
188	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34 -	232.34	6.78	06/2012 -	06/2012	0(O)	0/0
189	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95 -	2,360.95	1,620.54	08/2012 -	08/2012	0(O)	0/0
190	765 KV POOLING STATION & NETWORK WITH DVC AND MAIT - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	3,704.90	08/2012 -	08/2012	0(O)	0/0
191	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83 -	1,216.83	262.82	08/2012 -	08/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
192	TRANSMISSION SYSTEM ASSOCIATED WITH MUNDRA ULTRA M - [N18000061]PGCIL,Multi State	10/2008	4,824.12	4,824.12	1,084.73	10/2012	10/2012	0(O)	0/0
193	MAUDA TRANSMISSION SYSTEM - [N18000084]PGCIL,Maharashtra	02/2010	469.38	469.38	92.07	10/2012	10/2012	0(O)	0/0
194	INTERCONNECTION BETWEEN ELECTTRICAL GRIDS OF I - [N18000089]PGCIL,Multi State	10/2010	160.32	160.32	11.23	10/2012	10/2012	0(O)	0/0
195	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2007	5,459.28	6,010.89	2,392.00	08/2012	11/2012	3(O)	0/0
196	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99	4,672.99	261.44	11/2012	11/2012	0(O)	0/0
197	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58	965.58	171.89	11/2012	11/2012	0(O)	0/0
198	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80	1,272.80	85.21	11/2012	11/2012	0(O)	0/0
199	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38	1,061.38	940.15	09/2009	12/2012	39(O)	0/0
200	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88	7,031.88	2,185.46	12/2012	12/2012	0(O)	0/0
201	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00	5,915.00	1,877.00	10/2012	12/2012	2(O)	0/0
202	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81	6,230.81	1,727.00	10/2012	12/2012	2(O)	0/0
203	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00	2,144.00	186.94	12/2012	12/2012	0(O)	0/0
204	NORTHERN REGION SYSTEM STRENGHTENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68	182.68	25.54	01/2013	01/2013	0(O)	0/0
205	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03	250.03	17.35	01/2013	01/2013	0(O)	0/0
206	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pr.	10/2002	4,527.15	4,527.15	3,639.00	04/2009	03/2013	47(O)	19/41
207	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69	477.69	337.21	09/2010	03/2013	30(O)	0/0
208	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Orissa	09/2010	2,074.86	2,074.86	99.43	03/2013	03/2013	0(O)	0/0
209	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57	1,677.57	62.92	04/2013	04/2013	0(O)	0/0
210	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VELLUR - [N18000097]PGCIL,Multi State	08/2010	170.36	170.36	8.70	04/2013	04/2013	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
211	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM - [N18000090]PGCIL,Andhra Pradesh	12/2010	779.21	779.21	54.88	08/2013	05/2013	-3(O)	0/0
212	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01	623.44	64.92	01/2012	07/2013	18(O)	0/0
213	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64	752.64	33.00	07/2013	07/2013	0(O)	0/0
214	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pr.	12/2008	573.99	573.99	185.69	08/2013 08/2013	08/2013	0(R3)	8/17
215	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19	11,130.19	2,366.21	08/2013	08/2013	0(O)	0/0
216	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII - [N18000091]PGCIL,Multi State	12/2010	209.78	209.78	15.15	08/2013	08/2013	0(O)	0/0
217	ESTABLISHMENT OF POOLING STATION AT RAIGHAR AND RA - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52	1,719.52	122.97	08/2013	08/2013	0(O)	0/0
218	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pr.	01/2007	2,047.03	2,047.03	1,153.21	01/2012	09/2013	20(O)	2/10
219	BONGAIGAON THERMAL POWER PROJECT (NTPC) - [N18000041]NTPC,Assam	01/2008	4,375.35	4,375.35	2,173.00	07/2011	10/2013	27(O)	0/0
220	BARH STPP STAGE -II (NTPC) - [N18000047]NTPC,Bihar	02/2008	7,341.04	7,341.04	2,173.00	08/2013	10/2013	2(O)	0/0
221	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL,Multi State	03/2011	1,585.12	1,585.12	55.83	11/2013	11/2013	0(O)	0/0
222	LOWER SUBANSIRI H.E.P (NHPC) - [180100221]NHPC,Arunachal Pr.	09/2003	6,285.33	6,285.33	4,904.40	09/2010	12/2013	39(O)	2/11
223	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Orissa	12/2010	2,743.19	2,743.19	210.01	12/2013	12/2013	0(O)	0/0
224	TUIRIAL HE PROJECT(NEEPCO) - [180100165]NEEPCO,Mizoram	07/1998	368.72 913.63	913.63	227.58	07/2006 01/2014	01/2014	0(R3)	2/5
225	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttaranchal	11/2006	2,978.48	2,978.48	1,109.00	03/2013	02/2014	11(O)	5/31
226	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL,Multi State	03/2011	2,569.25	2,569.25	-	03/2014	03/2014	0(O)	0/0
227	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pr.	09/2002	3,919.59	3,919.59	3,137.19	09/2009	07/2014	58(O)	1/20
228	BARH STPP STAGE-I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,693.00	8,692.97	5,688.00	11/2010	09/2014	46(O)	15/51
229	Transm System for development of Pooling stn. in N - [N18000077]PGCIL,West Bengal	04/2010	4,404.57	4,404.57	-	01/2015	01/2015	0(O)	0/0
230	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,	07/2006	1,657.00	2,978.86	258.47	07/2010	03/2015	56(O)	0/1

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
231	KISHANGANGA HEP - [N18000031]NHPC,J & K	07/2007	2,238.67	3,642.04	707.10	07/2014	01/2016	18(O)	0/0
232	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttaranchal	08/2008	2,221.31	2,491.58	149.13	07/2014	03/2016	20(O)	0/8
233	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pr.	12/2004	2,496.90	2,496.90	1,438.50	12/2009 06/2016	06/2016	0(R3)	78/21
234	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45 1,007.16	947.96	756.41	12/2007 12/2009	-	-	14/18
	Total		178,558.19	184,085.59	82,495.45				237/499
	Railways								
235	DALLIRAJDHARA - RAOGHAT(PART OF DALLIRAJHARA-JAGDALPUR),NL,R - [220100149]RVNL,Chhatisgarh	04/1995	304.00	968.60	-	12/2012	12/2012	0(O)	0/0
236	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16	243.40	-	- 02/2009	12/2010	22(R1)	0/0
237	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	211.90	-	- 03/2009	12/2010	21(R1)	0/0
238	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62	221.90	-	12/2007 03/2010	12/2010	9(R1)	0/0
239	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL,Uttar Pradesh	04/2003	230.73 399.73	399.50	-	03/2009 12/2008	12/2010	24(R1)	0/0
240	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSION - [N22000081]RVNL,Gujarat	09/2005	200.80	200.80	-	- -	12/2010	-	0/0
241	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52	273.00	-	- 03/2009	03/2011	24(R1)	0/0
242	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00	329.70	-	03/2009 12/2009	03/2011	15(R1)	0/0
243	ALUABARI ROAD SILIGURI JANCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	415.50	352.97	- -	03/2011	-	0/0
244	MUMBAI URBAN TRANSPORT PROJECT PHASE-I, MTP - [N22000093]MRTP,Maharashtra	04/2003	3,125.20 4,174.40	4,501.80	4,145.31	- 12/2010	06/2011	6(R3)	0/1
245	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97	723.27	371.15	06/2005 07/2011	07/2011	0(R3)	0/0
246	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	700.00	144.72	- -	08/2011	-	0/0
247	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.90	170.00	179.17	03/2002 -	09/2011	114(O)	0/0
248	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50	252.50	-	02/2010 -	11/2011	21(O)	0/0
249	GUNA-ETAWAH(NCR), NL - [220100007]NCR,Multi State	04/1985	158.77 432.46	540.96	538.15	03/1994 -	12/2011	213(O)	0/0
250	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 164.36	429.49	425.27	02/2009 -	12/2011	34(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
251	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, Orissa	04/1996	301.64 -	735.10	-	- 09/2009	12/2011	27(R1)	0/0
252	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR, Orissa	04/2005	726.96 810.78	810.78	72.76	- -	12/2011	-	0/0
253	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR, Karnataka	04/2007	482.00 -	482.00	177.86	03/2013 -	12/2011	-15(O)	0/0
254	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER, Uttar Pradesh	03/1997	395.00 1,062.36	1,577.46	1,058.17	- -	02/2012	-	0/0
255	Ghutarisharif-Canning (ER) - [N22000117]ER, West Bengal	04/2009	189.97 -	189.97	43.97	12/2011 -	02/2012	2(O)	0/0
256	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, Andhra Pradesh	12/1994	124.43 407.78	617.63	469.21	- -	03/2012	-	0/0
257	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR, Karnataka	04/1996	157.00 262.82	262.82	181.02	- 03/2012	03/2012	0(R3)	0/0
258	MUZAFFARPUR-SITAMARHI(NL), ECR - [220100194]ECR, Bihar	04/1997	100.00 322.29	411.22	396.55	- -	03/2012	-	0/0
259	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]ECR, Bihar	04/1997	233.00 335.77	903.56	517.88	- -	03/2012	-	0/0
260	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR, Bihar	04/1996	114.01 283.95	427.89	331.59	- 03/2011	03/2012	12(R3)	0/0
261	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU, Bihar	04/2003	98.74 224.51	337.30	175.15	- -	03/2012	-	0/0
262	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU, Bihar	03/2005	470.09 1,417.97	1,417.97	813.57	- -	03/2012	-	0/0
263	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL, Chhatisgarh	09/2006	324.90 -	324.90	-	03/2010 -	03/2012	24(O)	0/0
264	CONSTRUCTION OF NEW LINE FROM HARMATI-TANAGAR/NAR - [N22000083]NEFR, Arunachal Pr.	09/1996	156.00 -	254.29	160.86	- -	03/2012	-	0/0
265	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE, Uttar Pradesh	02/2008	171.10 -	171.10	74.98	03/2012 -	03/2012	0(O)	0/0
266	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE, Uttar Pradesh	12/2004	129.17 -	220.00	165.75	03/2011 -	03/2012	12(O)	0/0
267	Sadulpur-Bikaner and Ratangarh-Degana Gauge Canves - [N22000106]NWR, Rajasthan	04/2007	643.36 -	803.39	724.40	03/2011 -	03/2012	12(O)	0/0
268	Tinpahar - Sahibganj (ER) - [N22000115]ER, Jharkhand	04/2008	167.73 -	167.73	34.30	03/2012 -	03/2012	0(O)	0/0
269	Rattam-Mhow-Khandwa-Akola (GC) - [N22000120]WR, Madhya pradesh	04/2008	603.04 -	603.04	27.61	03/2012 -	03/2012	0(O)	0/0
270	Bhuj-Naliya(GC) with extension from naliyate vayor - [N22000123]WR, Gujarat	04/2008	318.24 -	318.24	0.13	03/2012 -	03/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
271	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	730.00	316.65	- 07/2012	07/2012	0(R3)	0/0
272	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	273.67 1,160.52	1,404.00	548.07	- -	12/2012	-	0/0
273	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44 576.27	1,104.40	529.95	12/2012 -	12/2012	0(O)	0/0
274	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 -	1,211.22	377.28	03/2005 12/2008	12/2012	48(R1)	0/0
275	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	401.83	218.10	- 03/2012	12/2012	9(R3)	0/0
276	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 -	341.41	205.61	- -	12/2012	-	0/0
277	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 -	981.00	443.67	03/2009 -	12/2012	45(O)	0/0
278	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 -	1,389.00	901.38	10/2007 -	12/2012	62(O)	0/0
279	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	687.20	-	03/2010 -	12/2012	33(O)	0/0
280	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 -	207.52	97.17	12/2012 -	12/2012	0(O)	0/0
281	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	356.87	140.11	- 03/2013	03/2013	0(R3)	0/0
282	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	139.03	- -	03/2013	-	0/0
283	RANGIA-MURKONGSELEK, (GC) NEFR - [220100315]NEFR,Multi State	01/2004	915.70 912.70	1,556.23	572.80	- -	03/2013	-	0/0
284	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.13 -	350.81	-	03/2013 -	03/2013	0(O)	0/0
285	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 495.74	495.74	108.50	- 06/2013	06/2013	0(R3)	0/0
286	Dakshin-barasat-lakshmikantapur (ER) - [N22000116]ER,West Bengal	04/2009	259.51 -	259.51	50.71	12/2011 -	11/2013	23(O)	0/0
287	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	159.94	- -	12/2013	-	0/0
288	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 -	227.90	80.73	12/2012 -	12/2013	12(O)	0/0
289	Lumding-silchar jiribam, badarpur-baraigram kumarghat - [N22000127]NEFR,Multi State	04/1996	1,676.31 -	4,184.84	2,634.72	03/2009 -	12/2013	57(O)	0/0
290	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDG - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	3,230.01	2,171.12	04/2008 03/2014	03/2014	0(R3)	0/0
291	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 -	1,655.80	698.96	12/2008 -	03/2014	63(O)	0/0
292	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 -	1,141.76	167.04	03/2014 -	03/2014	0(O)	0/0
293	BHAIRABI SAIRONG, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	2,429.41	2.90	04/2014 -	03/2014	-1(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
294	New Work for Construction of Metro railway from Ba - [N22000109]RVNL, West Bengal	04/2010	2,069.60	2,069.60	0.21	03/2014	03/2014	0(O)	0/0
295	Jaipur - Ringus - Churu and Sikar - Lohatu Guage C - [N22000113]NWR, Rajasthan	04/2008	653.19	653.19	3.25	03/2014	03/2014	0(O)	0/0
296	Suratpura - Hanumangarh - Sriganganagar Guage Canv - [N22000114]NWR, Rajasthan	04/2008	516.23	516.23	3.29	03/2014	03/2014	0(O)	0/0
297	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR, Gujarat	04/2008	1,389.62	1,389.62	137.87	03/2014	03/2014	0(O)	0/0
298	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR), Uttar Pradesh	04/2006	325.00	369.90	92.88	03/2010 06/2014	06/2014	0(R3)	0/0
299	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR, Bihar	04/2003	324.66	324.66	156.52	-	03/2015	-	0/0
300	MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP - [N22000092]MRTP, Maharashtra	04/2008	5,300.00	5,300.00	206.42	03/2014	03/2015	12(O)	0/0
301	SEVOK RANGPO, NEFR - [N22000102]NEFR, Sikkim	04/2008	1,339.48	3,380.57	53.01	12/2015	03/2015	-9(O)	0/0
302	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR, Rajasthan	04/2008	829.74	829.74	-	03/2015	03/2015	0(O)	0/0
303	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR, Nagaland	04/2006	850.00	850.00	7.98	03/2015	03/2015	0(O)	0/0
304	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR, Multi State	04/2003	727.56 727.53	3,056.85	399.71	03/2011 03/2014	03/2016	24(R3)	0/0
305	New Work for Construction of Metro railway from No - [N22000108]RVNL, West Bengal	04/2010	2,397.72	2,397.72	-	03/2016	03/2016	0(O)	0/0
306	New Work for Construction of Metro railway from NS - [N22000110]RVNL, West Bengal	04/2010	3,951.98	3,951.98	1.42	03/2016	03/2016	0(O)	0/0
307	New Work for Construction of Metro railway - [N22000111]RVNL, West Bengal	04/2010	2,619.02	2,619.02	19.73	03/2016	03/2016	0(O)	0/0
308	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133](NR), J & K	03/1995	2,500.00 8,000.00	11,270.00	7,168.53	03/2001	12/2017	201(O)	0/0
309	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS, Multi State	03/1984	520.00 422.79	634.13	480.19	03/1995	-	-	0/0
310	RAJKOT-VERAVAL (GC) AND WANSJALIYA-JETALSAR GC AN - [220100116]WR, Gujarat	04/1992	112.53 320.66	464.50	507.10	03/1996 08/2009	-	-	0/0
311	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR, West Bengal	04/1983	36.80 274.41	415.23	233.02	-	-	-	0/0
312	CALICUT-MANGALORE (DL) (SR) - [220100151]SR, Multi State	02/1996	240.00	579.37	590.76	-	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
313	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 462.67	1,010.00	77.59	- -	-	-	0/0
314	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 -	412.91	453.52	- -	-	-	0/0
315	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 -	1,038.00	524.23	03/1998 -	-	-	0/0
316	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 -	712.00	529.51	- -	-	-	0/0
317	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00 -	997.58	63.54	- -	-	-	0/0
318	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	497.47	81.02	- -	-	-	0/0
319	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 154.30	499.16	130.92	03/2007 03/2007	-	-	0/0
320	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 -	363.26	0.27	07/2008 -	-	-	0/0
321	KODERMA-RANCHI VIA BARKAKHANA (NL),ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 1,099.20	1,099.20	1,001.04	07/2005 -	-	-	0/0
322	VILLUPURAM-KATPADI (GC)(SR) - [220100251]SR,Tamil Nadu	02/2000	175.00 -	513.16	537.51	- -	-	-	0/0
323	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	550.00	68.19	- -	-	-	0/0
324	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 -	162.87	86.25	- -	-	-	0/0
325	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30	847.76	808.28	06/2007 -	-	-	0/0
326	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	296.20	-	04/2003 03/2010	-	-	0/0
327	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 -	548.96	456.05	- -	-	-	0/0
328	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 -	695.00	9.44	- -	-	-	0/0
329	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 519.67	607.09	293.52	- 12/2012	-	-	0/0
330	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 -	901.62	0.29	- -	-	-	0/0
331	HAPUR-KANKATHER (LD),NR - [220100278](NR),Uttar Pradesh	04/2003	106.64 106.64	166.61	147.21	03/2007 05/2008	-	-	0/0
332	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91 -	418.17	69.85	- -	-	-	0/0
333	RAMGANJMUDDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	1,225.00	203.92	- -	-	-	0/0
334	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94 -	173.49	169.83	03/1998 08/2005	-	-	0/0
335	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23 -	638.00	-	02/2015 -	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
336	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	791.60	0.74	- -	-	-	0/0
337	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhandd	03/1997	186.92 -	261.70	-	02/2006 -	-	-	0/0
338	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	732.80	-	03/2008 06/2008	-	-	0/0
339	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 -	900.00	150.81	- -	-	-	0/0
340	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 -	900.00	364.50	- -	-	-	0/0
341	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 -	227.40	20.40	- -	-	-	0/0
342	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 -	582.83	73.17	- -	-	-	0/0
343	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	529.88	34.30	- -	-	-	0/0
344	KISHANGANJ JALALGARH, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 -	359.86	0.71	- -	-	-	0/0
345	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	488.76	428.94	06/1999 03/2011	-	-	0/0
346	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	495.44	163.20	03/2004 -	-	-	0/0
347	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhandd	04/1995	184.00 254.07	675.00	409.17	- 12/2011	-	-	0/0
348	AJMER-UDAIPUR-CHITTAURGARH (GC),NWR - [220100185]NWR,Rajasthan	09/1996	262.00 456.00	567.23	546.68	- 11/2010	-	-	0/0
349	SURENDRANAGAR-BHAVNAGAR(GC),WR - [220100187]WR,Gujarat	03/1997	437.40 589.86	563.25	544.24	03/2004 03/2010	-	-	0/0
350	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 281.20	281.20	325.54	- 03/2011	-	-	0/0
351	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhandd	04/1997	194.07 -	456.45	263.34	06/2004 04/2005	-	-	0/0
352	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	925.00	492.10	05/2008 03/2011	03/2011	0(R3)	0/0
353	AGRA-ETAWAH VIA FATEBAD & BAD (NL),NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	227.08	214.15	12/2009 03/2011	-	-	0/0
354	KATI HAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Multi State	09/2001	100.00 492.98	744.69	708.53	- 12/2010	-	-	0/0
355	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 863.23	863.23	287.38	- -	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
356	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 -	522.56	239.95	- -	-	-	0/1
357	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 -	1,029.00	657.58	- -	03/2013	-	0/0
358	DEOGHAR-DUMKA NEW BG LINE (DOUBL.) (ER) - [220100264]ER,Jharkhandd	02/1999	180.73 -	358.00	347.43	12/2006 02/2011	-	-	0/0
359	TOLLYGANJ-GARIA with extension to Dum Dum-Naopara - [220100268]MRTP,West Bengal	03/2000	907.69 1,032.76	2,812.07	2,708.44	12/2006 08/2010	-	-	0/0
360	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 108.91	228.09	224.82	- 02/2011	-	-	0/0
361	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 762.33	762.33	358.14	- 12/2009	-	-	0/0
362	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	475.28	450.62	02/2010 02/2011	-	-	0/0
363	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd	04/1996	371.36 -	452.35	342.10	- -	-	-	0/0
364	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/2001	143.92 258.60	258.60	93.38	- 03/2011	-	-	0/0
365	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 -	218.19	63.42	- -	-	-	0/0
366	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 -	230.03	126.80	- -	-	-	0/0
367	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322]WR,Gujarat	04/2005	148.61 -	227.52	256.07	03/2008 10/2010	-	-	0/0
368	SHIMOGA-TALAGUPPA (SWR), GC - [N22000056]SWR,Karnataka	12/1992	46.00 218.00	218.00	247.31	- 02/2011	-	-	0/0
369	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 -	384.04	46.05	- -	-	-	0/0
370	BARDHAMAN-KATWA, ER (GC) - [N22000091]ER,West Bengal	04/2007	245.15 -	245.15	130.15	12/2010 03/2011	-	-	0/0
371	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR,Gujarat	04/2006	196.97 -	196.97	142.15	03/2011 -	-	-	0/0
372	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 -	225.68	121.84	- 12/2010	-	-	0/0
373	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	196.95	166.10	03/2011 03/2011	03/2011	0(R3)	0/0
	Total		66,775.98 -	123,021.21	49,671.06				0/2
Road Transport & Highways									
374	MEHSI TO KOTWA (LMNHP-II), PH.II, KM.480 TO KM.440, NH-28 - [240106223]NHAI,Bihar	12/2003	239.00 -	239.00	317.60	07/2005 -	04/2011	69(O)	0/0
375	PURNEA-GOYAKOTA SEC.(EW) (NS & EW-PH-I) KM.419-KM.447, NH-31 - [240103191]NHAI,Bihar	04/2000	205.73 -	205.73	247.70	07/2004 -	05/2011	82(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
376	IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS - [240106203]NHAI,Tamil Nadu	12/2003	210.00 -	210.00	672.30	04/2007 -	05/2011	49(O)	0/0
377	GONDE-VADAPE(THANE), NH-3, KM.440/000 TO KM.539/500 - [240106262]NHAI,Maharashtra	03/2005	579.00 -	579.00	765.90	04/2009 -	05/2011	25(O)	0/0
378	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B - [240106276]NHAI,Tamil Nadu	03/2005	629.00 -	629.00	910.00	11/2010 -	05/2011	6(O)	0/0
379	NAGAON BYPASS (NH-37)(NHAI) - [240106289]NHAI,Assam	12/2003	230.00 -	230.00	312.00	06/2008 -	05/2011	35(O)	0/0
380	KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]NHAI,Uttar Pradesh	12/2003	242.00 -	242.00	362.70	12/2008 -	05/2011	29(O)	0/0
381	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	250.39	275.30	10/2008 -	05/2011	31(O)	0/0
382	THRISSUR TO ANGAMALI (NH-47) - [N24000037]NHAI,Kerala	12/2003	312.50 -	312.50	592.10	03/2009 -	05/2011	26(O)	0/0
383	JHANSI TO LALITPUR, NH-26 - [N24000097]NHAI,Uttar Pradesh	12/2003	276.09 -	276.09	294.90	09/2009 -	05/2011	20(O)	0/0
384	TRICHY - DINDIGUAL NH-45 - [N24000099]NHAI,Tamil Nadu	03/2005	576.00 -	576.00	614.00	07/2010 -	05/2011	10(O)	0/0
385	PONDICHERY - TINDIVANAU NH-66 - [N24000100]NHAI,Tamil Nadu	03/2005	285.00 -	285.00	355.80	07/2010 -	05/2011	10(O)	0/0
386	ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) - [N24000117]NHAI,Multi State	02/2008	295.00 -	295.00	622.90	08/2010 -	05/2011	9(O)	0/0
387	KALGHAT-MP/MAHARASHTRA BORDER KM 16.6-84.70 - [N24000119]NHAI,Madhya pradesh	11/2008	549.00 -	549.00	815.00	05/2010 -	05/2011	12(O)	0/0
388	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00 -	486.00	508.90	05/2010 -	05/2011	12(O)	0/0
389	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	196.65	135.40	08/2004 -	06/2011	82(O)	0/0
390	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	207.56	145.22	08/2004 -	06/2011	82(O)	0/0
391	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI,West Bengal	04/2000	273.00 -	522.00	465.70	03/2005 -	06/2011	75(O)	0/0
392	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI,Uttar Pradesh	12/2003	275.00 -	275.00	288.00	09/2007 -	06/2011	45(O)	0/0
393	HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	220.00	208.30	09/2007 -	06/2011	45(O)	0/0
394	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]NHAI,Gujarat	12/2003	412.78 -	479.54	435.80	11/2007 -	06/2011	43(O)	0/0
395	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2 - [240106222]NHAI,Uttar Pradesh	12/2003	193.00 -	193.00	321.10	10/2008 -	06/2011	32(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
396	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28 - [240106225]NHAI,Uttar Pradesh	12/2003	217.00	217.00	345.40	10/2008	06/2011	32(O)	0/0
397	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI,J & K	12/2003	193.09	166.30	167.60	03/2008	06/2011	39(O)	0/0
398	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J & K	12/2003	166.27	193.10	136.90	03/2008	06/2011	39(O)	0/0
399	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00	240.00	240.90	10/2008	06/2011	32(O)	0/0
400	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00 - [240106246]NHAI,Uttar Pradesh	12/2003	227.00	227.00	352.90	10/2008	06/2011	32(O)	0/0
401	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68	340.68	336.80	03/2008	06/2011	39(O)	0/0
402	MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00 - [240106256]NHAI,Uttar Pradesh	03/2005	359.00	359.00	772.80	03/2009	06/2011	27(O)	0/0
403	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00	190.00	227.00	01/2009	06/2011	29(O)	0/0
404	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI,Uttar Pradesh	12/2003	227.00	227.00	350.70	12/2008	06/2011	30(O)	0/0
405	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94	332.94	248.80	09/2008	06/2011	33(O)	0/0
406	LALITPUR TO SAGAR, NH-26 (NHAI) - [240106299]NHAI,Madhya pradesh	12/2003	198.00	198.00	170.10	11/2008	06/2011	31(O)	0/0
407	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03	251.03	247.20	10/2008	06/2011	32(O)	0/0
408	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI,Madhya pradesh	12/2003	229.91	229.91	197.60	10/2008	06/2011	32(O)	0/0
409	RINGBUNDS TO JHAJHANPUR (BR-6) - [N24000030]NHAI,Bihar	12/2003	340.00	340.00	535.10	06/2008	06/2011	36(O)	0/0
410	SITAPUR-LUCKNOW - [N24000036]NHAI,Uttar Pradesh	03/2005	322.00	322.00	553.70	06/2009	06/2011	24(O)	0/0
411	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27	263.27	242.30	02/2004	06/2011	88(O)	0/0
412	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI,Uttar Pradesh	12/2003	600.24	600.24	645.90	10/2009	06/2011	20(O)	0/0
413	KURALI-KIRATPUR, NH-21 - [N24000087]NHAI,Punjab	03/2005	309.00	309.00	553.60	06/2010	06/2011	12(O)	0/0
414	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00	604.00	411.90	12/2009	06/2011	18(O)	0/0
415	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06	355.06	294.40	09/2009	06/2011	21(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
416	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00	516.00	548.70	07/2010	06/2011	11(O)	0/0
417	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00	941.00	1,803.00	01/2011	06/2011	5(O)	0/0
418	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI,Karnataka	03/2005	441.00	441.00	802.70	07/2010	06/2011	11(O)	0/0
419	BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4 - [N24000106]NHAI,Karnataka	03/2005	565.00	565.00	1,060.00	07/2010	06/2011	11(O)	0/0
420	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70	228.70	132.29	02/2004	06/2011	88(O)	0/0
421	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI,Chhatisgarh	01/2008	464.00	464.00	419.90	01/2011	06/2011	5(O)	0/0
422	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI,Madhya pradesh	12/2003	225.00	225.00	236.40	10/2008	07/2011	33(O)	0/0
423	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50	196.50	221.20	06/2008	07/2011	37(O)	0/0
424	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00	168.00	385.30	12/2008	08/2011	32(O)	0/0
425	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75	1,693.75	2,258.00	08/2011	08/2011	0(O)	0/0
426	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82	221.82	212.70	11/2008	09/2011	34(O)	0/0
427	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00	241.53	60.78	04/2004	10/2011	90(O)	0/0
428	DAKOBA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00	225.00	238.90	06/2008	10/2011	40(O)	0/0
429	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37	353.37	171.50	10/2011	10/2011	0(O)	0/0
430	Chilkalripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30	572.30	498.30	10/2011	10/2011	0(O)	0/0
431	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI,Uttar Pradesh	12/2003	151.30	151.30	158.50	10/2008	11/2011	37(O)	0/0
432	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00	2,288.00	2,233.00	11/2011	11/2011	0(O)	0/0
433	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49	367.49	453.68	03/2005	12/2011	81(O)	0/0
434	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00	201.66	76.56	09/2008	12/2011	39(O)	0/0
435	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00	230.00	193.70	06/2005	12/2011	78(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
436	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	280.00	212.80	02/2009 -	12/2011	34(O)	0/0
437	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	200.00	73.55	04/2009 -	12/2011	32(O)	0/0
438	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	195.00	160.90	06/2008 -	12/2011	42(O)	0/0
439	BIJNI TO ASSAM WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	237.80	185.50	06/2008 -	12/2011	42(O)	0/0
440	SAGAR - RAJMARG CHORAH,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhy Pradesh	12/2003	203.43 -	203.43	181.40	10/2008 -	12/2011	38(O)	0/0
441	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar	12/2003	340.00 -	340.00	410.80	09/2008 -	12/2011	39(O)	0/0
442	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00 -	200.00	245.10	06/2008 -	12/2011	42(O)	0/0
443	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	264.72	229.40	06/2008 -	12/2011	42(O)	0/0
444	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00 -	245.00	458.60	03/2008 -	12/2011	45(O)	0/0
445	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00 -	225.00	160.90	06/2008 -	12/2011	42(O)	0/0
446	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00 -	208.00	192.40	04/2008 -	12/2011	44(O)	0/0
447	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00 -	160.00	108.50	05/2008 -	12/2011	43(O)	0/0
448	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	200.00	175.30	06/2008 -	12/2011	42(O)	0/0
449	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	280.00	579.30	06/2009 -	12/2011	30(O)	0/0
450	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]NHAI,Bihar	12/2003	418.04 -	418.04	290.60	03/2010 -	12/2011	21(O)	0/0
451	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56 -	390.56	278.20	02/2012 -	02/2012	0(O)	0/0
452	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47 -	154.57	167.90	09/2007 -	03/2012	54(O)	0/0
453	GUWAHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96 -	175.96	106.20	04/2008 -	03/2012	47(O)	0/0
454	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16 -	198.16	165.60	04/2008 -	03/2012	47(O)	0/0
455	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	217.61	118.70	04/2010 -	03/2012	23(O)	0/0
456	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	281.31	178.50	02/2010 -	03/2012	25(O)	0/0
457	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00 -	557.00	930.90	02/2010 -	05/2012	27(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
458	Pune-sholapur, pkg1 - [N24000127]NHAI, Maharashtra	11/2009	1,110.00	1,110.00	501.80	05/2012	05/2012	0(O)	0/0
459	Kishangarh-Ajmer-Beawer - [N24000128]NHAI, Rajasthan	11/2009	795.00	795.00	559.40	05/2012	05/2012	0(O)	0/0
460	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI, Andhra Pradesh	08/2010	388.00	388.00	246.60	05/2012	05/2012	0(O)	0/0
461	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI, Bihar	12/2003	300.00	300.00	151.10	10/2008	06/2012	44(O)	0/0
462	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI, Madhya pradesh	12/2003	300.93	300.93	293.90	10/2009	06/2012	32(O)	0/0
463	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI, Multi State	12/2003	232.45	232.45	157.00	09/2010	06/2012	21(O)	0/0
464	PATHANKOT BHOGPUR NH-1A - [N24000115]NHAI, Punjab	12/2003	229.00	284.00	322.00	05/2010	06/2012	25(O)	0/0
465	MP/Maharashtra Border-Dhula - [N24000126]NHAI, Maharashtra	12/2009	835.00	835.00	289.90	06/2012	06/2012	0(O)	0/0
466	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI, Multi State	04/2009	1,673.70	1,673.70	1,478.00	10/2011	06/2012	8(O)	0/0
467	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, Maharashtra	03/2005	940.00	940.00	298.60	07/2012	07/2012	0(O)	0/0
468	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]NHAI, Punjab	12/2003	284.00	359.00	101.40	05/2008	08/2012	51(O)	0/0
469	LAKHNAADON TO MP/MH BORDER, KM 596.75-653 (NS-1/BOT/MP-2), NH7 - [N24000094]NHAI, Madhya pradesh	12/2003	407.60	407.60	183.30	06/2010	10/2012	28(O)	0/0
470	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI, Madhya pradesh	12/2003	263.17	263.17	232.70	09/2009	10/2012	37(O)	0/0
471	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI, Maharashtra	04/2010	1,170.52	1,170.52	4.41	06/2011	10/2012	16(O)	0/0
472	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI, Gujarat	03/2010	1,509.10	1,509.10	670.90	09/2012	10/2012	1(O)	0/0
473	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI, Andhra Pradesh	04/2010	1,740.00	1,740.00	527.00	10/2012	10/2012	0(O)	0/0
474	AMRITSAR-PATHANKOT - [N24000147]NHAI, Punjab	05/2010	705.00	705.00	578.00	11/2012	11/2012	0(O)	0/0
475	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, West Bengal	12/2003	225.00	225.00	173.00	07/2008	12/2012	53(O)	0/0
476	Jaipur-Tonk-Deoli - [N24000135]NHAI, Rajasthan	06/2010	792.06	792.06	355.10	12/2012	12/2012	0(O)	0/0
477	Hazaribagh-Ranchi - [N24000141]NHAI, Jharkhand	08/2010	625.07	625.07	528.90	01/2013	01/2013	0(O)	0/0
478	Bijapur-Hungund Section - [N24000137]NHAI, Karnataka	09/2010	748.00	748.00	620.60	09/2010	03/2013	30(O)	0/0
479	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI, Karnataka	09/2010	946.00	946.00	-	03/2013	03/2013	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
480	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00	852.00	29.53	03/2013	03/2013	0(O)	0/0
481	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,Karnataka	09/2010	671.00	671.00	173.20	03/2013	03/2013	0(O)	0/0
482	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh	10/2010	1,175.00	1,175.00	138.70	04/2013	04/2013	0(O)	0/0
483	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00	1,585.00	112.50	05/2013	05/2013	0(O)	0/0
484	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16	348.16	110.80	09/2007	06/2013	69(O)	0/0
485	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81	385.13	29.60	04/2009	07/2013	51(O)	0/0
486	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04	280.13	39.26	11/2008	07/2013	56(O)	0/0
487	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	953.00	593.00	1.43	07/2013	07/2013	0(O)	0/0
488	New 4 Lane elevated road from chennai airport - [N24000139]NHAI,Tamil Nadu	09/2010	1,655.00	1,655.00	0.18	09/2013	09/2013	0(O)	0/0
489	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00	567.00	10.04	11/2013	11/2013	0(O)	0/0
490	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64	167.64	40.71	11/2008	12/2013	61(O)	0/0
491	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00	212.00	38.59	09/2007	12/2013	75(O)	0/0
492	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00	196.00	27.64	07/2009	12/2013	53(O)	0/0
	Total		52,920.82	54,384.23	43,500.17				0/0
	Shipping & Ports								
493	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40	2,427.40	820.72	10/2008	11/2010	25(O)	0/0
494	DEVELOPMENT OF COAL TERMINAL - [N25000055]ENNORE PORT LTD,Tamil Nadu	09/2006	399.13	399.13	-	08/2010	03/2011	7(O)	0/0
495	DEVELOPMENT OF IRON ORE TERMINAL - [N25000056]ENNORE PORT LTD,Tamil Nadu	09/2006	370.00	370.00	-	08/2010	04/2011	8(O)	0/0
496	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84 253.36	253.36	223.60	12/2007 07/2009	06/2011	23(R3)	0/0
497	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44	359.44	354.81	04/2011 06/2011	06/2011	0(R3)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
498	Construction & License out the OPERATION, MANAG. & - [N25000038]PORT TRUST,Karnataka	06/2006	230.00 -	272.50	219.00	12/2010 -	06/2011	6(O)	0/0
499	MARINE LIQUID TERMINALS - [N25000054]ENNORE TANK,Tamil Nadu	10/2004	196.25 -	196.25	-	06/2006 09/2011	09/2011	0(R2)	0/0
500	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]SHIPP.,Gujarat	01/2002	165.00 -	165.00	90.10	12/2005 01/2008	10/2011	45(R3)	0/0
501	Acquisition of two nos. of 120 B.P - [N25000042]PORT TRUST,Maharashtra	04/2009	290.85 -	290.85	86.46	06/2011 01/2012	01/2012	0(R3)	0/0
502	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]SHIPP.,Maharashtra	11/2007	1,061.96 -	1,061.96	240.52	03/2012 -	03/2012	0(O)	0/0
503	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]SHIPP.,Tamil Nadu	10/2002	150.00 600.00	600.00	38.00	03/2006 -	03/2012	72(O)	0/0
504	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	277.00	0.04	03/2012 -	03/2012	0(O)	0/0
505	Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST,Maharashtra	04/2009	277.03 -	277.03	55.41	12/2011 05/2012	05/2012	0(R3)	0/0
506	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	269.69	12/2010 09/2012	09/2012	0(R3)	0/0
507	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91 -	968.35	222.91	09/2012 -	09/2012	0(O)	0/0
508	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	29(O)	0/0
509	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 -	612.72	61.31	12/2012 -	12/2012	0(O)	0/0
510	C/O Berthing and Allied Facilities off tekra near - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,060.00	0.16	02/2011 -	03/2013	25(O)	0/0
511	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	0.73	03/2011 -	03/2013	24(O)	0/0
512	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]PORT TRUST,Kerala	03/2008	375.00 272.50	272.50	-	01/2009 -	05/2013	52(O)	0/0
513	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 -	1,028.10	202.04	12/2013 -	12/2013	0(O)	0/0
514	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	966.46	189.92	02/2014 -	02/2014	0(O)	0/0
515	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 -	800.00	4.63	10/2008 -	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	Total		14,464.19	15,317.65	3,080.05				0/0
	<u>Telecommunications</u>								
516	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]BSNL,Maharashtra	09/2008	1,799.94	1,799.94	50.11	09/2009	02/2010	5(O)	0/0
517	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00	425.51	102.34	12/2005	10/2010	58(O)	0/0
518	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88	952.88	-	03/2010	10/2010	7(O)	0/0
519	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65	152.65	-	03/2010	10/2010	7(O)	0/0
520	Procurement of DXC equipment - [N26000074]BSNL,Multi State	02/2008	229.00	229.00	-	03/2010	11/2010	8(O)	0/0
521	NIB-II PROJECT RURAL BROADBAND - [N26000037]BSNL,Multi State	12/2007	312.86	353.00	210.69	02/2008	12/2010	34(O)	0/0
522	Procurement of 2.5G DWDM equipment - [N26000066]BSNL,Multi State	08/2006	424.00	424.00	-	03/2009	12/2010	21(O)	0/0
523	Procurement of 10G 40 CHL (12 chi equipped) DWDM - [N26000068]BSNL,Multi State	12/2007	545.50	545.50	-	03/2010	12/2010	9(O)	0/0
524	Procurement of STM-1 SDH equipment - [N26000069]BSNL,Multi State	02/2007	154.03	154.03	-	03/2010	12/2010	9(O)	0/0
525	Procurement of STM-16 MADM equipment - [N26000070]BSNL,Multi State	03/2008	355.92	355.92	-	03/2010	12/2010	9(O)	0/0
526	Procurement of STM-16 ADM equipment - [N26000071]BSNL,Multi State	02/2007	477.00	477.00	-	03/2010	12/2010	9(O)	0/0
527	GSM equipment of 375000Lines (2G) 75000lines 3(G) - [N26000085]BSNL,West Bengal	06/2008	170.23	170.23	127.26	06/2009	01/2011	19(O)	0/0
528	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 - [N26000040]BSNL,Haryana	01/2008	192.48	192.48	110.82	03/2009	02/2011	23(O)	0/0
529	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94	373.94	171.01	12/2008	02/2011	26(O)	0/0
530	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL,Orissa	11/2007	277.34	377.54	128.29	03/2009	02/2011	23(O)	0/0
531	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL,Uttaranchal	01/2009	149.15	158.72	25.67	06/2009	02/2011	20(O)	0/0
532	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81	336.81	105.16	01/2009	02/2011	25(O)	0/0
533	GSM equipment of 975000Lines (2G) 325000 lines 3(G) - [N26000083]BSNL,Uttar Pradesh	02/2009	625.53	625.53	19.52	02/2010	02/2011	12(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
534	GSM equipment of 945000Lines (2G) 225000lines 3(G) - [N26000086]BSNL,Bihar	10/2007	366.00	529.32	112.89	10/2008	02/2011	28(O)	0/0
535	GSM equipment of 1900000Lines (2G) 401700 lines 3(- [N26000091]BSNL,Tamil Nadu	01/2009	760.20	1,312.52	579.17	- 03/2011	02/2011	-1(R3)	0/1
536	GSM equipment of 1500000Lines (2G) 264700lines 3(G) - [N26000093]BSNL,Andhra Pradesh	01/2009	922.91	922.91	161.71	01/2010	02/2011	13(O)	0/0
537	GSM equipment of 1900000Lines (2G) 335500lines 3(G) - [N26000094]BSNL,Kerala	01/2009	848.70	848.70	399.04	01/2010	02/2011	13(O)	0/0
538	GSM equipment of 614000Lines (2G) 150000lines 3(G) - [N26000095]BSNL,Tamil Nadu	01/2009	315.19	315.19	68.99	01/2010	02/2011	13(O)	0/0
539	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) - [N26000039]BSNL,Rajasthan	06/2007	601.49	601.49	438.00	12/2008	03/2011	27(O)	0/0
540	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]BSNL,Uttar Pradesh	05/2007	335.91	335.91	140.73	03/2009	03/2011	24(O)	0/0
541	GSM equipment of 900000Lines (2G) PunjabPhase V.2 - [N26000081]BSNL,Punjab	09/2008	241.49	601.49	480.57	09/2009	03/2011	18(O)	0/0
542	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84	336.84	22.06	10/2009	03/2011	17(O)	0/0
543	GSM equipment of 1100000Lines (2G) UP East Phase - [N26000084]BSNL,Uttar Pradesh	09/2009	624.75	624.75	11.21	09/2010	03/2011	6(O)	0/0
544	GSM equipment of 849862Lines (2G) 150138 lines 3(G) - [N26000087]BSNL,West Bengal	02/2008	584.33	584.33	171.99	02/2009	03/2011	25(O)	0/0
545	GSM equipment of 1867000Lines (2G) 383000 lines 3(- [N26000089]BSNL,Gujarat	08/2008	868.00	868.00	191.48	08/2009	03/2011	19(O)	0/0
546	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70	916.70	151.70	11/2010	03/2011	4(O)	0/0
547	GSM equipment of 1700000Lines (2G) 234100 lines 3(- [N26000092]BSNL,Karnataka	10/2008	677.75 719.90	719.90	238.44	10/2009	03/2011	17(O)	0/0
548	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00	384.00	12.01	10/2010	04/2011	6(O)	0/0
549	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	229.41	66.20	02/2007	08/2011	54(O)	0/0
550	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00	247.00	75.89	02/2007	08/2011	54(O)	0/0
551	FTTH BO-3474 /08-09 in Mumbai - [N26000078]MTNL,Maharashtra	04/2010	389.86	389.86	3.06	09/2011	09/2011	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
552	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38	168.30	94.13	10/2007	-	-	0/0
553	MANAGED LEASED LINE NETWORK PH-VI - [N26000063]BSNL,Multi State	11/2008	350.00	350.00	-	-	-	-	0/0
554	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00	1,077.00	841.00	03/2009	-	-	0/0
555	Procurement of 10G (40 chl) DWDM equipment - [N26000067]BSNL,Multi State	08/2006	590.10	590.10	-	03/2009	-	-	0/0
556	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhand	03/2008	328.13	392.44	-	03/2009	-	-	0/0
	Total		20,025.99	21,450.84	5,311.14				0/1
			-						
	<u>Urban Development</u>								
557	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18	181.30	79.96	04/2009	01/2011	21(O)	0/0
			173.08			-			
558	DELHI MRTS PHASE-II PROJECT - [280100002]DMRC,Delhi	08/2005	8,676.00	18,894.36	17,548.44	06/2010	06/2011	12(O)	0/10
			8,605.36			-			
559	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00	11,609.00	2,267.57	12/2011	03/2013	15(O)	6/6
			-			-			
	Total		15,185.18	30,684.66	19,895.97				6/16
			-						
	<u>Water Resources</u>								
560	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90	1,187.00	35.49	12/2007	12/2012	60(O)	0/0
			-			-			
	Total		542.90	1,187.00	35.49				0/0
			-						
Grand Total			603,783.35	728,399.46	321,667.26				817/2057

Sector wise current status of projects on theFlash Report

Telecommunications


I. Current Status:

Number of Projects	41
Number of Projects On Schedule	1
Number of Projects Delayed	3

Number of Projects Without Date Of Commissioning 37

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 41 projects, 1 project are on schedule and 3 projects are delayed .37 projects do not have fixed dates of commissioning.

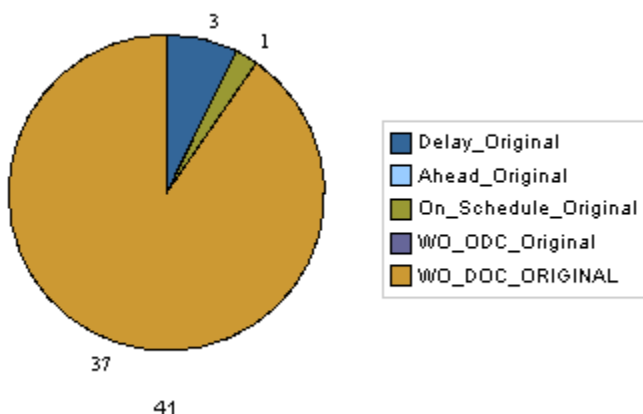

III. Investment Scenario

The Total Original cost of implementation of 41 projects when sanctioned, was of the order of Rs. 20025.99 crore but this was subsequently revised to Rs. 21450.84 crore implying a cost overrun of 7.1%. The expenditure incurred on these projects till April, 2011 is Rs. 5311.14 crore, which is 24.8% of the revised cost of the projects.

Figures are in Rs. Crore

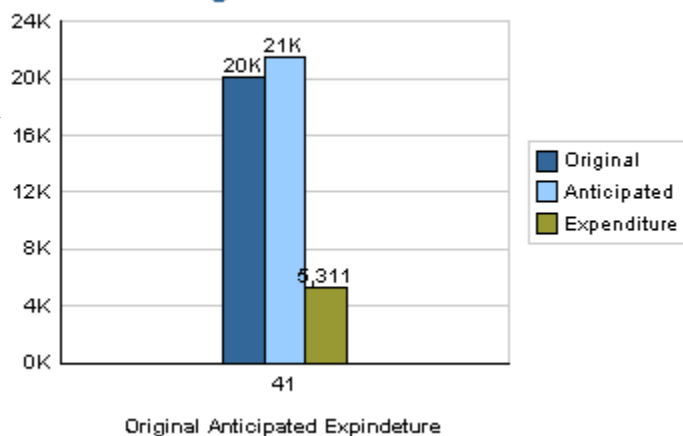

Sector wise current status of projects on theFlash Report


Steel

I. Current Status:

Number of Projects	13
Number of Projects Delayed	5
Number of Projects Without Original Date of Commissioning	8

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 13 projects, 5 projects are delayed .8 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

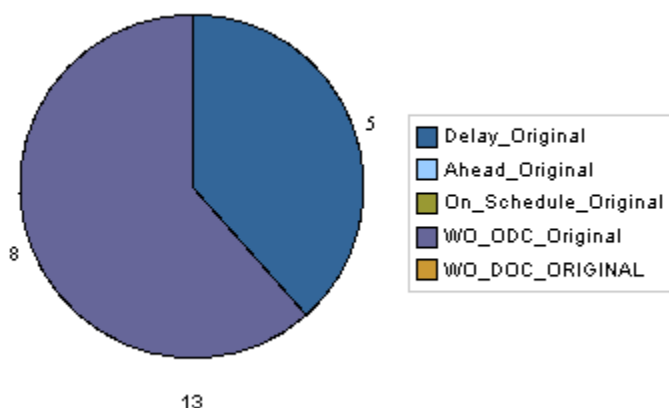

III. Investment Scenario

The Total Original cost of implementation of 13 projects when sanctioned, was of the order of Rs. 39927.85 crore but this was subsequently revised to Rs. 65040.88 crore implying a cost overrun of 62.9%. The expenditure incurred on these projects till April, 2011 is Rs. 24683.66 crore, which is 38% of the revised cost of the projects.

Figures are in Rs. Crore

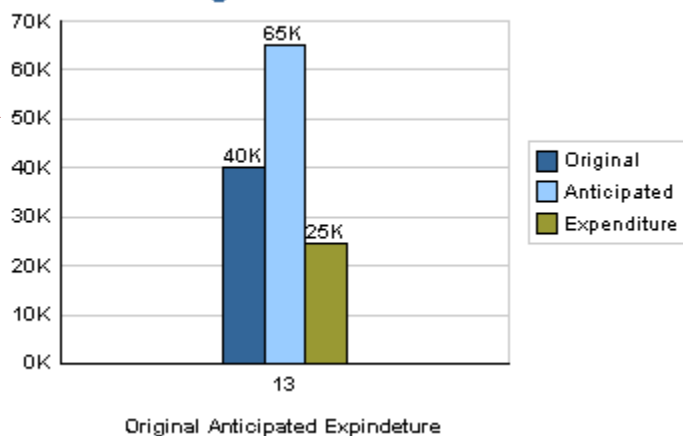

Sector wise current status of projects on theFlash Report

Shipping & Ports


I. Current Status:

Number of Projects	23
Number of Projects On Schedule	6
Number of Projects Delayed	14

Number of Projects Without Date Of Commissioning	3
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 23 projects, 6 projects are on schedule and 14 projects are delayed .3 projects do not have fixed dates of commissioning.

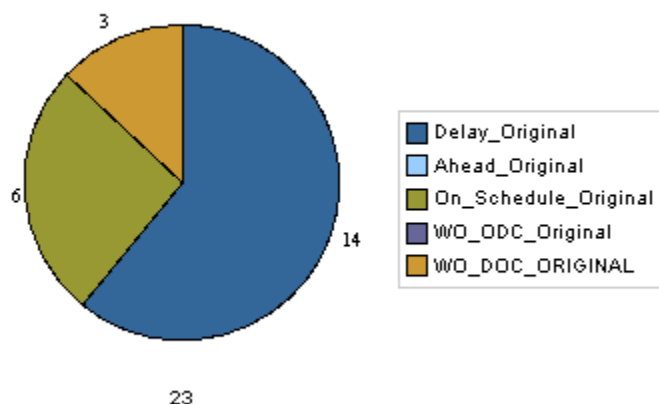

III. Investment Scenario

The Total Original cost of implementation of 23 projects when sanctioned, was of the order of Rs. 14464.19 crore but this was subsequently revised to Rs. 15317.65 crore implying a cost overrun of 5.9%. The expenditure incurred on these projects till April, 2011 is Rs. 3080.05 crore, which is 20.1% of the revised cost of the projects.

Figures are in Rs. Crore

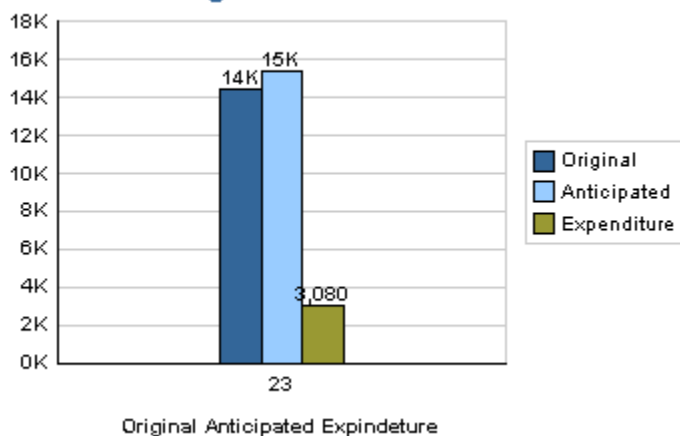

Sector wise current status of projects on theFlash Report


Road Transport & Highways

I. Current Status:

Number of Projects	119
Number of Projects On Schedule	22
Number of Projects Delayed	97

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 119 projects, 22 projects are on schedule and 97 projects are delayed .

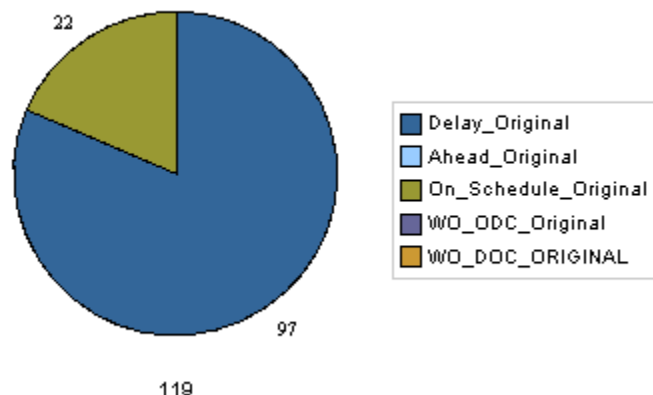

III. Investment Scenario

The Total Original cost of implementation of 119 projects when sanctioned, was of the order of Rs. 52920.82 crore but this was subsequently revised to Rs. 54384.23 crore implying a cost overrun of 2.8%. The expenditure incurred on these projects till April, 2011 is Rs. 43500.17 crore, which is 80% of the revised cost of the projects.

Figures are in Rs. Crore

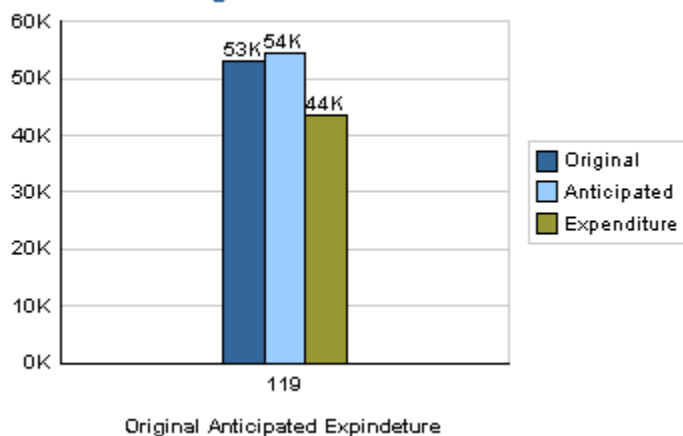

Sector wise current status of projects on theFlash Report


Railways

I. Current Status:

Number of Projects	139
Number of Projects On Schedule	18
Number of Projects Delayed	22
Number of Projects Ahead	3
Number of Projects Without Original Date of Commissioning	26
Number of Projects Without Date Of Commissioning	70

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 139 projects, 3 projects are ahead of schedule, 18 projects are on schedule and 22 projects are delayed. 70 projects do not have fixed dates of commissioning. 26 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

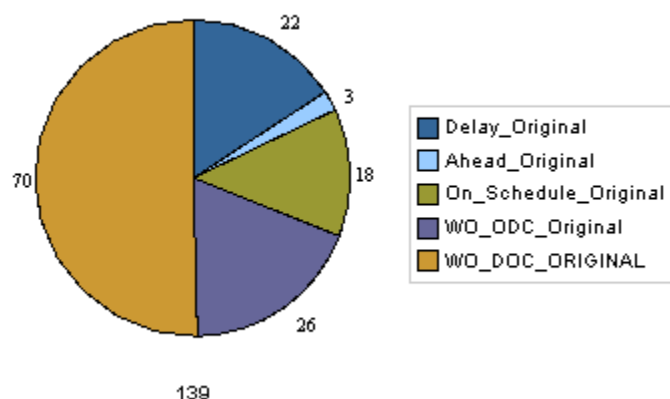

III. Investment Scenario

The Total Original cost of implementation of 139 projects when sanctioned, was of the order of Rs. 66775.98 crore but this was subsequently revised to Rs. 123021.21 crore implying a cost overrun of 84.2%. The expenditure incurred on these projects till April, 2011 is Rs. 49671.06 crore, which is 40.4% of the revised cost of the projects.

Figures are in Rs. Crore

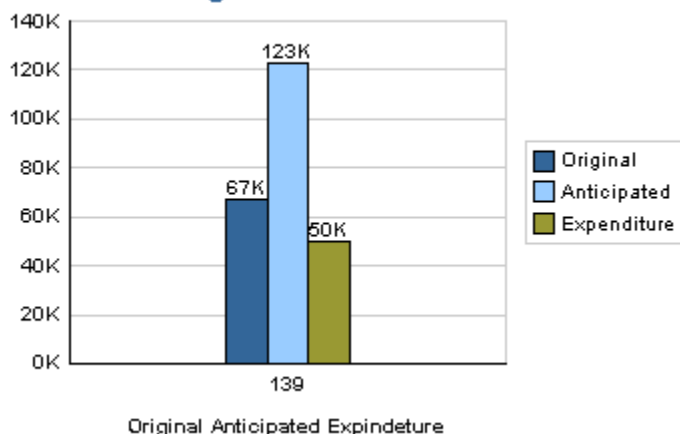

Sector wise current status of projects on theFlash Report


Power

I. Current Status:

Number of Projects	86
Number of Projects On Schedule	39
Number of Projects Delayed	44
Number of Projects Ahead	2
Number of Projects Without Date Of Commissioning	1

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 86 projects, 2 projects are ahead of schedule, 39 projects are on schedule and 44 projects are delayed. 1 project do not have fixed dates of commissioning.

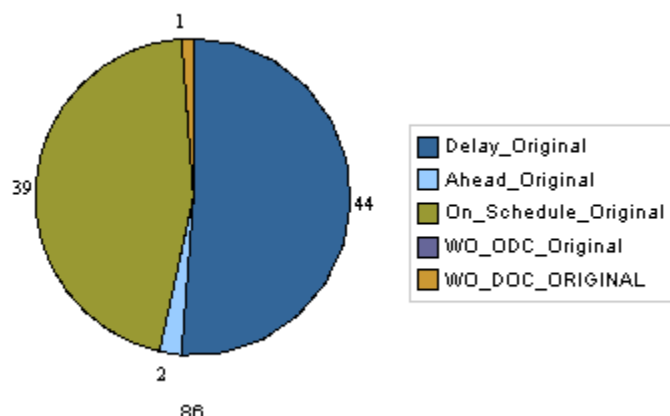

III. Investment Scenario

The Total Original cost of implementation of 86 projects when sanctioned, was of the order of Rs. 178558.19 crore but this was subsequently revised to Rs. 184085.59 crore implying a cost overrun of 3.1%. The expenditure incurred on these projects till April, 2011 is Rs. 82495.45 crore, which is 44.8% of the revised cost of the projects.

Figures are in Rs. Crore

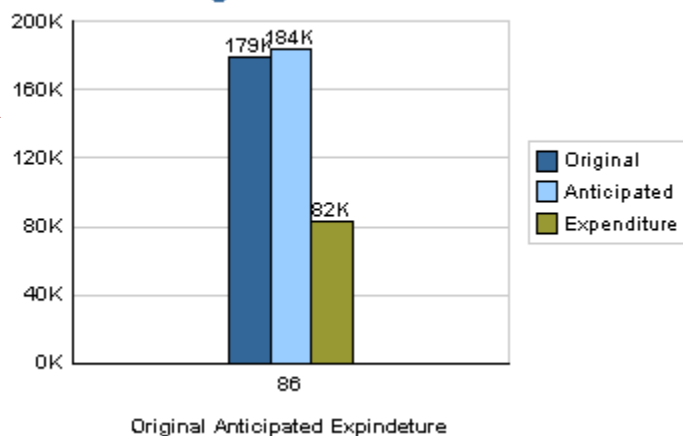

Sector wise current status of projects on theFlash Report


Petroleum

I. Current Status:

Number of Projects	73
Number of Projects On Schedule	22
Number of Projects Delayed	34
Number of Projects Ahead	5
Number of Projects Without Original Date of Commissioning	10
Number of Projects Without Date Of Commissioning	2

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 73 projects, 5 projects are ahead of schedule, 22 projects are on schedule and 34 projects are delayed. 2 projects do not have fixed dates of commissioning. 10 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

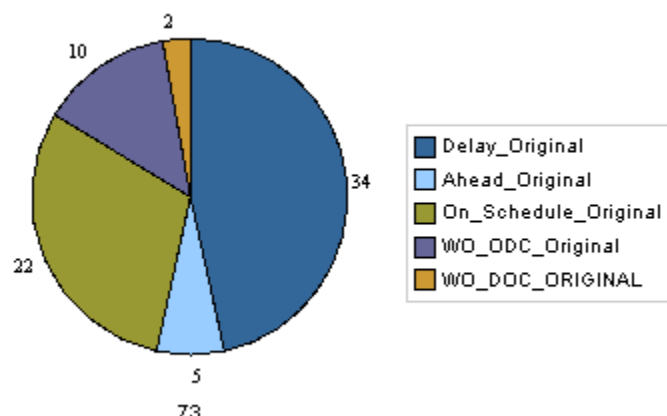

III. Investment Scenario

The Total Original cost of implementation of 73 projects when sanctioned, was of the order of Rs. 157868.41 crore but this was subsequently revised to Rs. 167284.98 crore implying a cost overrun of 6%. The expenditure incurred on these projects till April, 2011 is Rs. 58101.99 crore, which is 34.7% of the revised cost of the projects.

Figures are in Rs. Crore

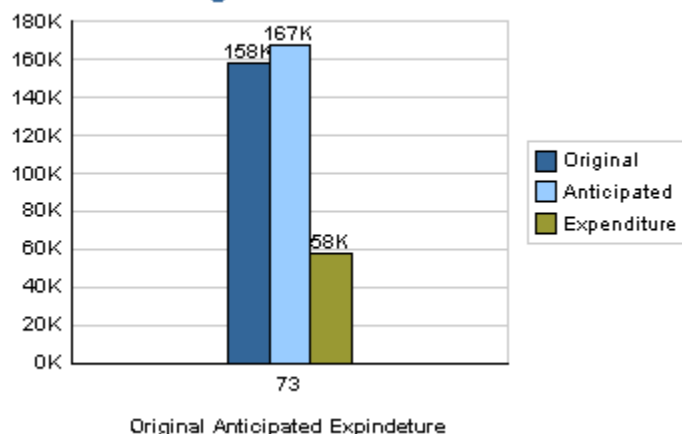

Sector wise current status of projects on theFlash Report


Coal

I. Current Status:

Number of Projects	45
Number of Projects On Schedule	23
Number of Projects Delayed	22

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 45 projects, 23 projects are on schedule and 22 projects are delayed .

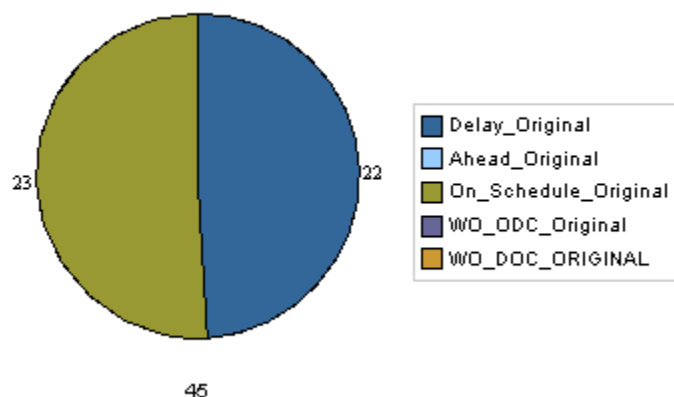

III. Investment Scenario

The Total Original cost of implementation of 45 projects when sanctioned, was of the order of Rs. 25509.15 crore but this was subsequently revised to Rs. 28789.48 crore implying a cost overrun of 12.9%. The expenditure incurred on these projects till April, 2011 is Rs. 10641.28 crore, which is 37% of the revised cost of the projects.

Figures are in Rs. Crore

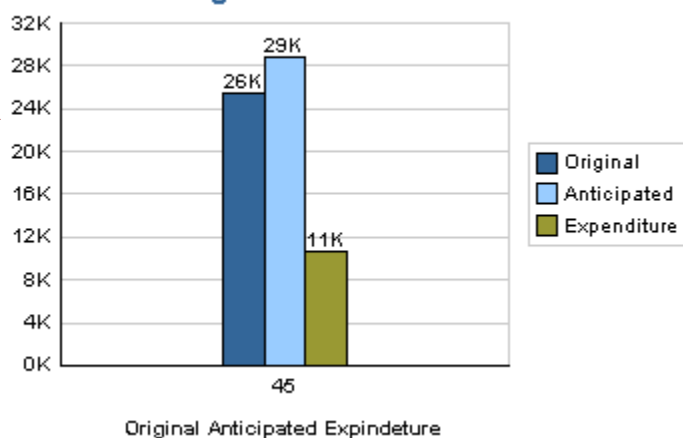

Sector wise current status of projects on theFlash Report

Civil Aviation


I. Current Status:

Number of Projects	7
Number of Projects On Schedule	2
Number of Projects Delayed	3

Number of Projects Without Date Of Commissioning	2
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 7 projects, 2 projects are on schedule and 3 projects are delayed .2 projects do not have fixed dates of commissioning.

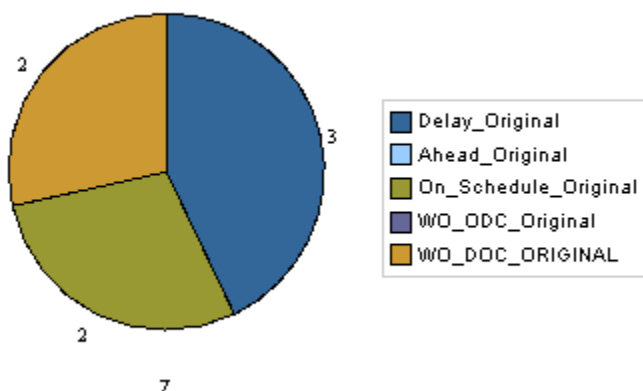

III. Investment Scenario

The Total Original cost of implementation of 7 projects when sanctioned, was of the order of Rs. 4826.48 crore but this was subsequently revised to Rs. 4826.48 crore implying a cost overrun of 0%. The expenditure incurred on these projects till April, 2011 is Rs. 2464.47 crore, which is 51.1% of the revised cost of the projects.

Figures are in Rs. Crore

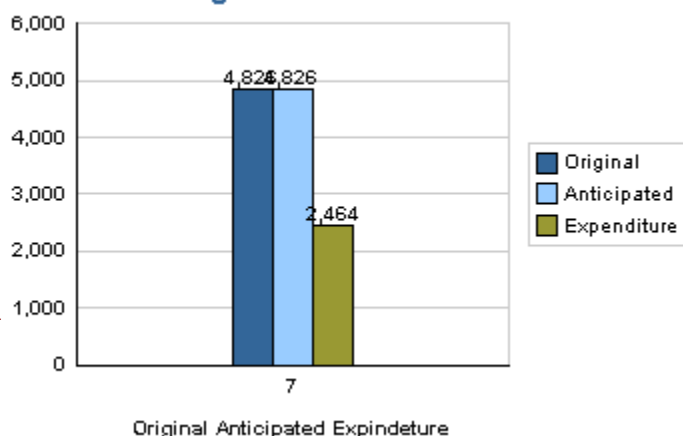

Sector wise current status of projects on theFlash Report


Atomic Energy

I. Current Status:

Number of Projects	3
Number of Projects Delayed	2
Number of Projects Without Original Date of Commissioning	1

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 3 projects, 2 projects are delayed .1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

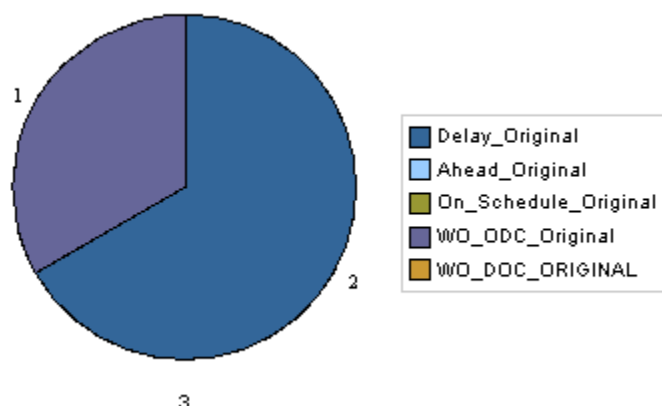

III. Investment Scenario

The Total Original cost of implementation of 3 projects when sanctioned, was of the order of Rs. 17769.29 crore but this was subsequently revised to Rs. 22607.29 crore implying a cost overrun of 27.2%. The expenditure incurred on these projects till April, 2011 is Rs. 17723.14 crore, which is 78.4% of the revised cost of the projects.

Figures are in Rs. Crore

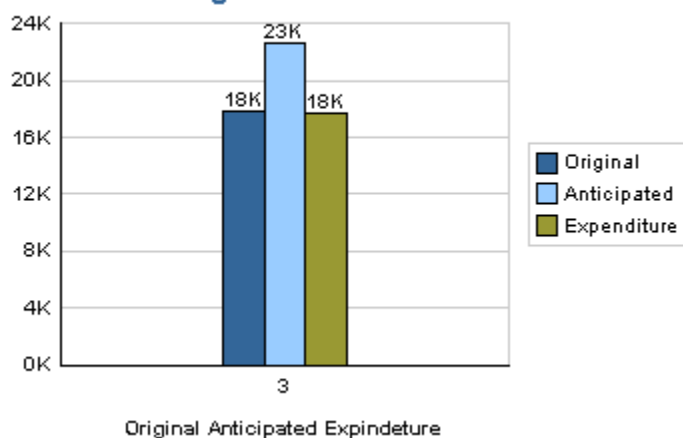

ANNEXURES

SUMMARY OF STATE WISE PROJECTS AS ON 01.05.2011

SN	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMMULATIVE EXPENDITURE
1	Andhra Pradesh	31	30947.82	36480.33	17698.96
2	Arunachal Pr.	4	9512.22	9610.51	6689.45
3	Assam	37	22540.13	28005.68	14567.38
4	Bihar	27	27513.33	31452.72	18284.07
5	Chhatisgarh	19	22504.86	37937.78	14025.71
6	Delhi	2	8925.00	19123.77	17614.64
7	Goa	1	204.73	204.73	32.50
8	Gujarat	26	19491.34	20457.76	4298.87
9	Haryana	10	4821.32	6546.83	4064.07
10	Himachal Pr.	7	15023.26	15105.54	11545.59
11	J & K	8	8293.37	18455.56	11085.25
12	Jharkhandd	21	9612.58	14445.17	5777.78
13	Karnataka	21	27652.42	35040.98	13846.95
14	Kerala	6	5235.00	6482.11	5239.77
15	Madhya pradesh	25	18938.72	18543.21	6488.83
16	Maharashtra	49	70088.08	84094.96	33007.78
17	Mizoram	2	988.06	3343.04	230.48
18	Multi State	106	120189.48	130154.23	44401.90
19	Nagaland	1	850.00	850.00	7.98
20	Orissa	26	51981.30	59843.75	13060.68
21	Punjab	9	5163.69	6509.65	2962.00
22	Rajasthan	16	13438.03	14167.15	7924.26
23	Sikkim	2	1603.77	3644.86	189.57
24	Tamil Nadu	36	43747.83	52878.94	34441.99
25	Tripura	3	1522.39	2018.86	277.02
26	Uttar Pradesh	31	15876.67	18071.40	9897.13
27	Uttaranchal	7	8777.62	11457.08	4088.77
28	West Bengal	27	38340.33	43472.86	19917.88
TOTAL		560	603783.35	728399.46	321667.26

LIST OF PROJECTS WITHOUT ORIGINAL DATE OF COMMISSIONING AS ON 01.05.2011

SN	NAME	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED
Atomic Energy				
1	URANIUM ORE MINE & PROCESSING PLANT AT TUMMALAPALLE	N.A.	04/2011	04/2012
Fertilisers				
2	THAL AMMONIA REVAMP PROJECT	N.A.	11/2011	11/2011
Petroleum				
3	Assam gas Cracker project	N.A.	N.A.	04/2012
4	HYDROCRACKER REVAMP & SETTING UP A NEW CCR AT MUMBAI REFINERY	N.A.	12/2011	01/2012
5	BAWANA NANGAL PIPE LINE PROJECT	N.A.	12/2011	12/2011
6	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I	N.A.	06/2011	06/2011
7	INTEGRATED OFFSHORE CRUDE OIL HANDLING FACILITIES AT PARADIP	N.A.	N.A.	06/2012
8	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT	N.A.	N.A.	02/2013
9	PARADIP REFINERY PROJECT	N.A.	N.A.	11/2012
10	PARADIP-RAIPUR-SAMBALPUR- RANCHI PIPELINE	N.A.	N.A.	09/2012
11	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pipeline)	N.A.	N.A.	08/2013
12	Fluidized catalytic cracking unit(FCCU) revamp at Mathura Refinery	N.A.	N.A.	01/2013
Railways				
13	JIND-SONEPAT (NL),NR	N.A.	03/2012	12/2012
14	NANGALDAM-TALWARA(NL),NR	N.A.	07/2012	07/2012
15	TALCHER-BIMALAGARH(NL)(ECOR)	N.A.	N.A.	12/2011
16	KHURDA ROAD-BOLANGIR(NL)ECOR	N.A.	N.A.	08/2011
17	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	N.A.	03/2011	03/2012
18	MUZAFFARPUR-SITAMARHI(NL),ECR	N.A.	N.A.	03/2012
19	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	N.A.	N.A.	03/2015
20	KOSI BRIDGE (NL), ECR	N.A.	N.A.	12/2012
21	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	N.A.	N.A.	03/2012
22	DEOGHAR - SULTANGANJ (INL), ER	N.A.	12/2012	N.A.
23	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	N.A.	12/2011	N.A.
24	MUMBAI URBAN TRANSPORT PROJECT PHASE-I, MTP	N.A.	12/2010	06/2011
25	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	N.A.	06/2013	06/2013
26	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR	N.A.	N.A.	03/2012
27	RANGIA-MURKONGSELEK, (GC) NEFR	N.A.	N.A.	03/2013
28	KANPUR-KASGANJ-MATHURA(GC),NER	N.A.	N.A.	02/2012
29	DAUSA-GANGAPUR CITY(NL),NWR	N.A.	N.A.	03/2013
30	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR	N.A.	N.A.	12/2012
31	HARIDASPUR-PARADEEP(NL)	N.A.	09/2009	12/2011
32	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	N.A.	N.A.	03/2012
33	CHHINDWARA - NAGPUR (GC)(SECR)	N.A.	N.A.	12/2013

SN	NAME	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED
34	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	N.A.	N.A.	03/2013
35	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR)	N.A.	03/2012	03/2012
36	VIRAMGAM-BHILDI(WR),GC	N.A.	03/2013	03/2013
37	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS&PU	N.A.	N.A.	03/2012
38	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT	N.A.	N.A.	03/2012
Steel				
39	Bailadila Iron Ore Deposit- II(B)(NMDC)	N.A.	N.A.	10/2011
40	330 TPH BOILER-6 AND AUXILIARY SYSTEM	N.A.	N.A.	09/2011
41	COKE OVEN BATTERY NO. 4 PHASE-II	N.A.	10/2012	10/2012
42	Augmentation of Iron Ore Storage in RMHP	N.A.	05/2012	05/2012
43	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREMENT EXP. UNIT	N.A.	N.A.	09/2011
44	EXPANSION OF BOKARO STEEL PLANT	N.A.	12/2011	12/2011
45	EXPANSION OF BHILAI STEEL PLANT	N.A.	03/2013	03/2013
46	INSTALLATION OF 700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI	N.A.	N.A.	07/2011

LIST OF PROJECTS WITHOUT DATE OF COMMISSIONING AS ON 01.05.2011

SN	NAME	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED
	Civil Aviation			
1	D/O OF TERMINAL BLDG. AND PAVEMENT WORKS AT CHENNAI AIRPORT	06/2010	N.A.	N.A.
2	CONSTRUCTION OF RCC/PRE STRESSD CONCRETE BRIDGE ACROSS THE ADYAR AT CHENNAI AIRPORT(k3)	09/2010	N.A.	03/2011
	Petroleum			
3	CAPACITY EXP. CUM MODERNISATION PH-II	12/2009	N.A.	12/2010
4	JHAJJAR HISSAR PIPE LINE PROJECT	10/2010	N.A.	N.A.
	Power			
5	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL)	12/2007	12/2009	N.A.
	Railways			
6	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR)	03/2008	10/2010	N.A.
7	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	03/1995	N.A.	N.A.
8	KISHANGANJ JALALGARH, NEFR	N.A.	N.A.	N.A.
9	BARDHAMAN-KATWA, ER (GC)	12/2010	03/2011	N.A.
10	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	N.A.	N.A.	N.A.
11	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	N.A.	N.A.	N.A.
12	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSION	N.A.	N.A.	12/2010
13	RAICHUR-GUNTAKAL(DL)(SCR)	12/2007	03/2010	12/2010
14	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL)	03/2009	12/2009	03/2011
15	MANOHARABAD-KOTHPALL NEW LINE(SCR)	N.A.	N.A.	N.A.
16	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL)	03/2009	12/2008	12/2010
17	GOELKERA-MANOHARPUR,(LD)(SER)	02/2006	N.A.	N.A.
18	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	03/2008	06/2008	N.A.
19	SHIMOGA-TALAGUPPA (SWR), GC	N.A.	02/2011	N.A.
20	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY'-AGASTHAMPALLI	N.A.	N.A.	N.A.
21	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	N.A.	N.A.	N.A.
22	TOLLYGANJ-GARIA with extension to Dum Dum-Naopara and Noapara-NSCB Airport(MTP)	12/2006	08/2010	N.A.
23	GADWAL - RAICHUR (NL), SCR	N.A.	02/2011	N.A.
24	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	N.A.	12/2009	N.A.
25	BANGLORE - SATYAMANGALAM (NL)(SWR)	N.A.	N.A.	N.A.
26	HAPUR-KANKATHER (LD),NR	03/2007	05/2008	N.A.
27	REWARI-ROHTAK (NL),NR	02/2010	02/2011	N.A.
28	RAJATGARH-BARANG(LD),ECOR	N.A.	02/2009	12/2010
29	KODERMA-TILAIYA (NL), ECR	N.A.	N.A.	N.A.
30	KODERMA GIRIDH (NL), ECR	N.A.	N.A.	N.A.
31	VILLUPURAM-KATPADI (GC)(SR)	N.A.	N.A.	N.A.
32	ANGAMALI-SABARIMALA (N.L.)(SR)	N.A.	N.A.	N.A.
33	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER)	N.A.	N.A.	N.A.
34	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	N.A.	N.A.	N.A.
35	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	06/2007	N.A.	N.A.
36	RENIGUNTA-GUNTAKAL(RE)	04/2003	03/2010	N.A.
37	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	N.A.	N.A.	N.A.

38	DEOGHAR-DUMKA NEW BG LINE (DOUBL.)(ER)	12/2006	02/2011	N.A.
39	KOTLPALLI-NARASAPUR (NL) (SCR)	N.A.	N.A.	N.A.
40	SRIGANGANAGAR-SARUPSAR (GC), NWR	N.A.	03/2011	N.A.
41	RAMGANJMUNDI-BHOPAL (NL),WCR	N.A.	N.A.	N.A.
42	MAHARAJGANJ-MASRAKH (NL) - NER	N.A.	N.A.	N.A.
43	HATHUA-BHATNI (N L) (NER)	N.A.	N.A.	N.A.
44	BILASPUR-URKURA (DL)	N.A.	03/2009	03/2011
45	RUPSA-BANGRIPOSI (GC)(SER)	03/1998	08/2005	N.A.
46	SUKINDA ROAD - ANGUL (NL)(ECOR)	02/2015	N.A.	N.A.
47	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	N.A.	03/2009	12/2010
48	MUNEERABAD-MAHABOBNAGAR(NL),SCR	N.A.	N.A.	N.A.
49	HOWRAH-AMTA-CHAMPADANGA NL (SER)	03/2007	03/2007	N.A.
50	KOTTUR-HARIHAR(NL),(SWR)	N.A.	03/2011	N.A.
51	RANCHI-LOHARDAGA(GC),SER	06/2004	04/2005	N.A.
52	MACHERLA-NALGONDA(NL)(SCR)	07/2008	N.A.	N.A.
53	KODERMA-RANCHI VIA BARKAKHANA (NL),ECR	07/2005	N.A.	N.A.
54	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	05/2008	03/2011	03/2011
55	AGRA-ETAWAH VIA FATEBAD AND BAD (NL) NCR	12/2009	03/2011	N.A.
56	KATIHAR - JOGBANI (GC)(NEFR)	N.A.	12/2010	N.A.
57	RAJKOT-VERAVAL (GC) AND WANSJALIYA-JETALSAR GC AND VERAVAL SOMNATH NL(WR)	03/1996	08/2009	N.A.
58	AMRAVATI-NARKHER NL(CR)	06/1999	03/2011	N.A.
59	New BG line Rly line from Eklakhi-Balurghat including Gazole-Itahar(NL),NEFR	N.A.	N.A.	N.A.
60	CALICUT-MANGALORE (DL) (SR)	N.A.	N.A.	N.A.
61	BELAPUR-SEAWOOD-URAN ELECTRIF-IED DOUBLE LINE(MTP)	03/2004	N.A.	N.A.
62	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	N.A.	N.A.	N.A.
63	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR	N.A.	N.A.	N.A.
64	AJMER-CHITTAURGARH -UDAIPUR-UMRA (GC),NWR	N.A.	11/2010	N.A.
65	GONDIA-JABALPUR(GC),(SECR)	03/1998	N.A.	N.A.
66	SURENDRANAGAR-BHAVNAGAR(GC),WR	03/2004	03/2010	N.A.
67	KARUR-SALEM(NL),SR	N.A.	N.A.	N.A.
68	HUBLI-ANKOLA(NL),SWR	N.A.	N.A.	N.A.
69	ALUABARI ROAD SILIGURI JANCTION VIA GALGALIA, NEFR	N.A.	N.A.	03/2011
70	TIDIVANAM-NAGARI (NL)	N.A.	N.A.	N.A.
71	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	N.A.	N.A.	N.A.
72	RAJPIPLA-ANKELASHWAR, WR (GC)	03/2011	N.A.	N.A.
73	Pandabeswar-Chinpai doubling (ER)	N.A.	12/2010	N.A.
74	Bhavnagar-workshop facilities for 50 BG coaches POH per month (WR)	03/2011	03/2011	03/2011
75	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	N.A.	N.A.	N.A.
Shipping & Ports				
76	DEVELOPMENT OF COAL TERMINAL	08/2010	N.A.	03/2011
77	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL	10/2008	N.A.	N.A.
78	SETHUSAMUDRAM SHIP CHANNEL PROJECT	10/2008	N.A.	11/2010
Telecommunications				

79	GSM equipment of 1900000Lines (2G) 401700 lines 3(G)Tamil Nadu Phase V.1 Telecom Circle	N.A.	03/2011	02/2011
80	GSM equipment of 945000Lines (2G) 225000lines 3(G) Bihar Phase V.1 Telecom Circle	10/2008	N.A.	02/2011
81	GSM equipment of 375000Lines (2G) 75000lines 3(G) Kolkatta Phase V.1 Telecom Circle	06/2009	N.A.	01/2011
82	GSM equipment of 1625000Lines (2G) 325000 lines 3(G) MP Phase V.1 Telecom Circle	11/2010	N.A.	03/2011
83	Procurement of 10G 40 CHL (12 chi equipped) DWDM equipment (SDCA level)	03/2010	N.A.	12/2010
84	GSM equipment of 799000Lines (2G) 101000 lines 3(G) JharkhandPhase V.1 Telecom Circle	03/2009	N.A.	N.A.
85	PROJ.III OF NIB-II OF MESSAGING STORAGE	12/2005	N.A.	10/2010
86	GSM equipment of 200000Lines (2G) UP(West)Phase V.2 Telecom Circle	10/2009	N.A.	03/2011
87	Procurement of STM-16 ADM equipment	03/2010	N.A.	12/2010
88	GSM equipment of 1867000Lines (2G) 383000 lines 3(G) GujaratPhase V.1 Telecom Circle	08/2009	N.A.	03/2011
89	GSM equipment of 1100000Lines (2G) UP East Phase V.2 Telecom Circle	09/2010	N.A.	03/2011
90	GSM equipment of 975000Lines (2G) 325000 lines 3(G) UP East Phase V.1 Telecom Circle	02/2010	N.A.	02/2011
91	Procurement of DXC equipment	03/2010	N.A.	11/2010
92	Procurement of STM-16 MADM equipment	03/2010	N.A.	12/2010
93	GSM equipment of 900000Lines (2G) PunjabPhase V.2 Telecom Circle	09/2009	N.A.	03/2011
94	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 9920/05-06	10/2007	N.A.	N.A.
95	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G)PH-5	12/2008	N.A.	03/2011
96	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1	03/2009	N.A.	02/2011
97	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) PH-5.1	12/2008	N.A.	02/2011
98	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) PH-5.1	03/2009	N.A.	02/2011
99	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN UP(W)-PH-V.I	03/2009	N.A.	03/2011
100	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G)	06/2009	N.A.	02/2011
101	Assam Telecom Circle, Phase-V.I, 2G & 3G	01/2009	N.A.	02/2011
102	Procurement of STM-1 SDH equipment	03/2010	N.A.	12/2010
103	MANAGED LEASED LINE NETWORK PH-VI	N.A.	N.A.	N.A.
104	GSM equipment of 1700000Lines (2G) 234100 lines 3(G)Karnataka Phase V.1 Telecom Circle	10/2009	N.A.	03/2011
105	GSM equipment of 849862Lines (2G) 150138 lines 3(G) West Bengal Phase V.1 Telecom Circle	02/2009	N.A.	03/2011
106	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3G) PH-5.1	09/2009	N.A.	02/2010
107	Implementation of FTTH, the state of the art Access Network,procurement of gepon equipment	03/2010	N.A.	10/2010
108	NIB-II PROJECT RURAL BROADBAND	02/2008	N.A.	12/2010
109	Procurement of 10G (40 chl) DWDM equipment	03/2009	N.A.	N.A.
110	Execution of telecom network requirement of defence forces	03/2009	N.A.	N.A.

111	GSM equipment of 614000Lines (2G) 150000lines 3(G) Chennai TD Phase V.1 Telecom Circle	01/2010	N.A.	02/2011
112	Implementation of FTTH, the state of the art access network.Procurement of gpon equipmant	03/2010	N.A.	10/2010
113	GSM equipment of 1500000Lines (2G) 264700lines 3(G)Andhra Pradesh Phase V.1 Telecom Circle	01/2010	N.A.	02/2011
114	GSM equipment of 1900000Lines (2G) 335500lines 3(G)kerala Phase V.1 Telecom Circle	01/2010	N.A.	02/2011
115	Procurement of 2.5G DWDM equipment	03/2009	N.A.	12/2010
	Urban Development			
116	C/o office building for IDBI at bandra Kurla Complex,Mumbai	04/2009	N.A.	01/2011

List of Projects Where in Revised cost Estimates'(s) is Required as on 01.05.2011

SN	PROJ_TITLE	DOA	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
All Cost in Rs. Crore					
	Atomic Energy				
1	KUDANKULAM APP (NPCIL)	12/2001	13171.00	0.00	13781.00
	Petroleum				
2	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT	09/2006	2305.30	700.00	2416.96
3	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2	10/2007	5713.03	0.00	6641.54
	Power				
4	CHAMERA,STAGE-III (NHPC)	08/2005	1405.63	0.00	1585.40
5	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC)	08/2006	621.28	0.00	634.74
6	KOTESHWAR HEP(THDC)	04/2000	1301.56	0.00	2348.18
7	NIMOO BAZGO HYDROELECTRIC PROJECT (NHPC)	08/2006	611.02	0.00	628.64
8	TESSTA LOW DAM - III HYDROELECTRIC POWER PROJECT (NHPC)	10/2003	768.92	0.00	1301.88
9	TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB GEN. PROJ.	04/2008	290.49	0.00	345.81
	Railways				
10	AGRA-ETAWAH VIA FATEBAD AND BAD (NL) NCR	04/1999	108.00	214.09	214.15
11	AJMER-CHITTAURGARH -UDAIPUR-UMRA (GC),NWR	09/1996	262.00	456.00	546.68
12	ALUABARI ROAD SILIGURI JANCTION VIA GALGALIA, NEFR	12/2006	170.00	170.00	352.97
13	AMRAVATI-NARKHER NL(CR)	06/1994	120.90	284.27	428.94
14	BANKURA - DAMODAR (GC) (SER)	03/1998	111.90	0.00	377.28
15	CALICUT-MANGALORE (DL) (SR)	02/1996	240.00	0.00	590.76
16	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR	09/1996	156.00	0.00	160.86
17	DEOGHAR-DUMKA NEW BG LINE (DOUBL.)(ER)	02/1999	180.73	0.00	347.43
18	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	09/2006	343.17	0.00	364.50
19	ELECTRIFICATION OF MORADABAD-ROZA	12/2004	129.17	0.00	165.75
20	GADWAL - RAICHUR (NL), SCR	04/1998	92.63	108.91	224.82
21	GONDIA-JABALPUR(GC),(SECR)	02/1997	386.30	0.00	524.23
22	GUNA-ETAWAH(NCR), NL	04/1985	158.77	432.46	538.15
23	HAPUR-KANKATHER (LD),NR	04/2003	106.64	106.64	147.21
24	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR	02/1997	295.00	0.00	453.52
25	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	03/2002	409.00	625.30	808.28
26	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	04/1997	233.00	335.77	517.88
27	KARUR-SALEM(NL),SR	02/1997	155.55	0.00	529.51
28	KATIHAR - JOGBANI (GC)(NEFR)	09/2001	100.00	492.98	708.53
29	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	04/1997	78.23	0.00	86.25
30	KOTTUR-HARIHAR(NL),(SWR)	04/1995	65.94	281.20	325.54
31	LANJHIGARH-JUNAGARH NL(ECOR)	04/1993	100.00	142.90	179.17
32	Lumding-silchar jiribam, badarpur-baraigram kumarghat national project	04/1996	1676.31	0.00	2634.72
33	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	04/1995	184.00	254.07	409.17

SN	PROJ_TITLE	DOA	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
All Cost in Rs. Crore					
34	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	04/1996	114.01	283.95	331.59
35	MUZAFFARPUR-SITAMARHI(NL),ECR	04/1997	100.00	322.29	396.55
36	NANDYAL-YERRAGUNTLA(NL),SCR	03/1996	155.74	164.36	425.27
37	PATNA GANGA BRIDGE (NL), ECR	04/2001	624.47	0.00	901.38
38	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	12/1994	124.43	407.78	469.21
39	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR)	04/2005	148.61	0.00	256.07
40	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	03/1998	280.00	0.00	657.58
41	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR	09/1997	1000.00	1500.00	2171.12
42	RAJKOT-VERAVAL (GC) AND WANSJALIYA-JETALSAR GC AND VERAVAL SOMNATH NL(WR)	04/1992	112.53	320.66	507.10
43	RANCHI-LOHARDAGA(GC),SER	04/1997	194.07	0.00	263.34
44	REWARI-ROHTAK (NL),NR	01/2004	149.38	330.23	450.62
45	RUPSA-BANGRIPOSI (GC)(SER)	02/1996	57.94	0.00	169.83
46	SHIMOGA-TALAGUPPA (SWR), GC	12/1992	46.00	218.00	247.31
47	Sadulpur-Bikaner and Ratangarh-Degana Gauge Canvession (NWR)	04/2007	643.36	0.00	724.40
48	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	293.97	0.00	371.15
49	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	09/1995	100.00	0.00	456.05
50	TOLLYGANJ-GARIA with extension to Dum Dum-Naopara and Noapara-NSCB Airport(MTP)	03/2000	907.69	1032.76	2708.44
51	VILLUPURAM-KATPADI (GC)(SR)	02/2000	175.00	0.00	537.51
Road Transport & Highways					
52	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2)	04/2000	367.49	0.00	453.68
53	AURANG-RAIPUR, NH-6, KM.232 TO KM.281	03/2005	190.00	0.00	227.00
54	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.250, NH-28	12/2003	193.00	0.00	321.10
55	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28	12/2003	217.00	0.00	345.40
56	BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4	03/2005	565.00	0.00	1060.00
57	DAKOBA TO NAGAON (NH-36)(NHAI)	12/2003	225.00	0.00	238.90
58	DELHI/ HARYANA BORDER TO ROHTAK	04/2007	486.00	0.00	508.90
59	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254	12/2003	412.78	0.00	435.80
60	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24	12/2003	275.00	0.00	288.00
61	GONDE-VADAPE(THANE), NH-3, KM.440/000 TO KM.539/500	03/2005	579.00	0.00	765.90
62	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRIDOR	12/2003	600.24	0.00	645.90
63	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00	12/2003	227.00	0.00	352.90
64	HALDIA PORT (PORT CONNECTIVITY) (NH-41)	04/2000	273.00	0.00	465.70
65	IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS	12/2003	210.00	0.00	672.30
66	JHAJHARPUR TO DARBANGA (BR-7)	12/2003	340.00	0.00	410.80
67	JHANSI TO LALITPUR, NH-26	12/2003	276.09	0.00	294.90

SN	PROJ_TITLE	DOA	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
All Cost in Rs. Crore					
68	KALGHAT-MP/MAHARASHTRA BORDER KM 16.6-84.70	11/2008	549.00	0.00	815.00
69	KASIA TO GORAKHPUR (NH-28)(NHAI)	12/2003	242.00	0.00	362.70
70	KOTA BYPASS,RJ-4, NH-76 (NHAI)	12/2003	275.00	0.00	275.30
71	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402	12/2003	240.00	0.00	240.90
72	KURALI-KIRATPUR, NH-21	03/2005	309.00	0.00	553.60
73	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI)	12/2003	225.00	0.00	236.40
74	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B	03/2005	629.00	0.00	910.00
75	MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00	03/2005	359.00	0.00	772.80
76	MEHSI TO KOTWA (LMNHP-II), PH.II, KM.480 TO KM.440, NH-28	12/2003	239.00	0.00	317.60
77	NAGAON BYPASS (NH-37)(NHAI)	12/2003	230.00	0.00	312.00
78	NAGPUR-KONDHALI,NH-6(NHAI)	03/2005	168.00	0.00	385.30
79	NALBARI TO BIJNI (AS-8)	12/2003	200.00	0.00	245.10
80	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVIHALLI	03/2005	441.00	0.00	802.70
81	NEW MANGALORE PORT NH-17 AND 48	04/2000	196.50	0.00	221.20
82	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	03/2005	557.00	0.00	930.90
83	PATHANKOT BHOGPUR NH-1A	12/2003	229.00	0.00	322.00
84	PONDICHERY - TINDIVANAU NH-66	03/2005	285.00	0.00	355.80
85	PURNEA-GOYAKOTA SEC.(EW) (NS AND EW-PH-I) KM.419-KM.447, NH-31	04/2000	205.73	0.00	247.70
86	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km)	05/2009	1108.00	0.00	2233.00
87	RINGBUNDS TO JHAJHANPUR (BR-6)	12/2003	340.00	0.00	535.10
88	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI)	12/2003	151.30	0.00	158.50
89	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68	03/2005	941.00	0.00	1803.00
90	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	12/2003	157.47	0.00	167.90
91	SITAPUR-LUCKNOW	03/2005	322.00	0.00	553.70
92	SONAPUR TO GUWAHTI (AS-3)	12/2003	245.00	0.00	458.60
93	Surat- Dahisar(Six Lane) Km 263 to Km 502	02/2009	1693.75	0.00	2258.00
94	THANJAUR-TRICHY,NH-67(NHAI)	03/2005	280.00	0.00	579.30
95	THRISSUR TO ANGAMALI (NH-47)	12/2003	312.50	0.00	592.10
96	TRICHY - DINDIGUAL NH-45	03/2005	576.00	0.00	614.00
97	TRICHY - KORUR NH-67	03/2005	516.00	0.00	548.70
98	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI)	12/2003	227.00	0.00	350.70
99	ZIRAKPUR(HARYANA) -PARWANOO(HIMACHAL PRADESH)	02/2008	295.00	0.00	622.90
Telecommunications					
100	GSM equipment of 900000Lines (2G) PunjabPhase V.2 Telecom Circle	09/2008	241.49	0.00	480.57
Urban Development					
101	DELHI MRTS PHASE-II PROJECT	08/2005	8676.00	8605.36	17548.44

Abbreviations used in the report

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro
LEP	Life Extension Program
LOI	Letter of Intent

LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Mining & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SSS	Sardar Swaran Singh
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
