


**318th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹ 150 Crores and above)
April, 2012**



AAI - Airport at Pakyong(Sikkim)

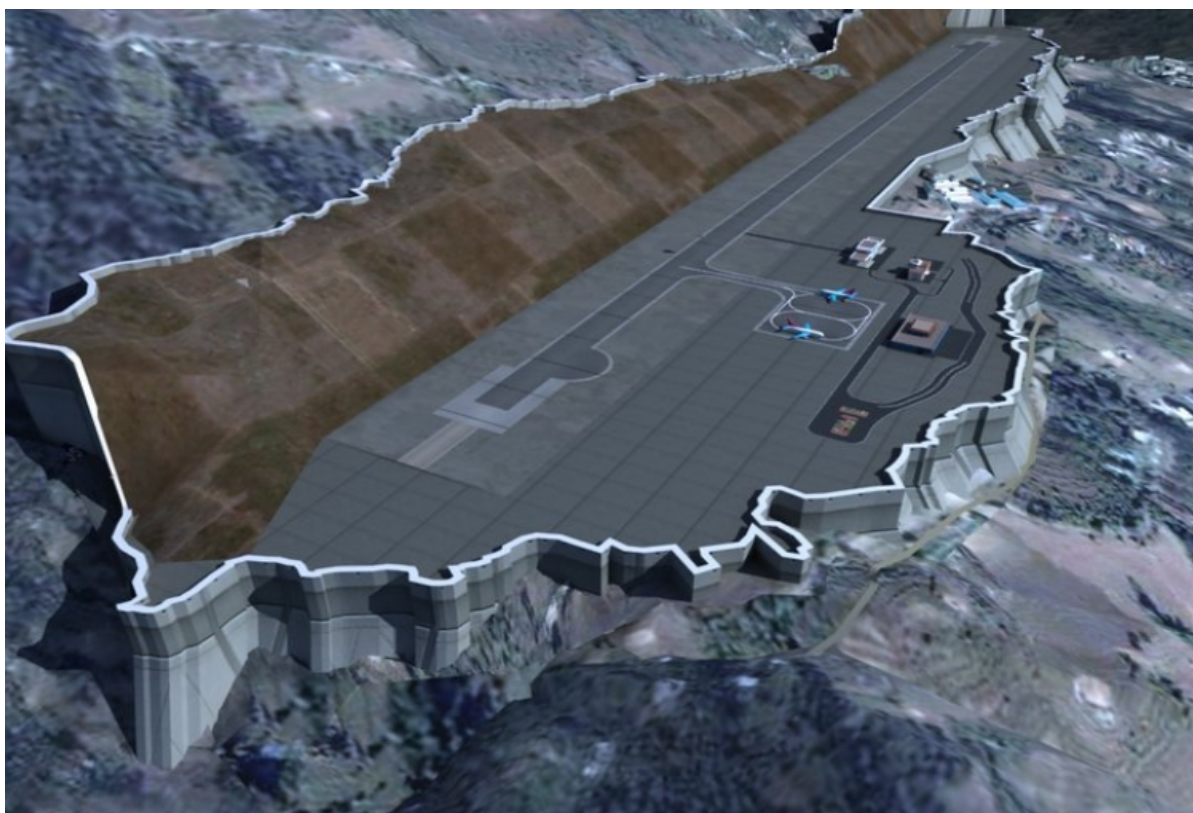

Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

EXECUTIVE SUMMARY

The Flash Report for April, 2012 contains information on the status of the 571 Central Sector Infrastructure Projects, costing ₹ 150 Crores and above. During, April, 2012, 8 projects (2 projects each of Shipping & Ports, Telecommunication , Road Transport & Highways and Power Sectors) have reported completion.

During the reference month, 54 projects have reported additional delays, vis-à-vis the date of completion reported in the previous month. The additional delays are in the range of 1 to 36 months, in respect of projects relating to Road Transport and Highways, Railways, Power, Petroleum, Coal, Shipping & Ports, Steel, and Telecommunication Sectors.

S. No.	Sector	Projects on monitor	Additional delays
1.	RAILWAYS	131	5
2.	ROAD TRANSPORT & HIGHWAYS	148	6
3.	POWER	102	23
4.	PETROLEUM	64	11
5.	COAL	51	3
6.	TELECOMMUNICATION	15	1
7.	SHIPPING & PORTS	22	1
8.	STEEL	16	4
9.	FERTILISERS	6	0
10.	CIVIL AVIATION	5	0
11.	ATOMIC ENERGY	5	0
12.	URBAN DEVELOPMENT	4	0
13.	WATER RESOURCES	1	0
14.	PETROCHEMICALS	1	0
Total		571	54

3. The total original cost of implementation of the 571 projects was about ₹ 7, 33,514.85 Crores and their anticipated completion cost is likely to be ₹ 8, 76,715.90 Crores, which

reflects an overall cost overrun of ₹1, 43,201.05 Crores (19.5 % of original cost). The expenditure incurred on these projects till April, 2012 is ₹ 3, 92,606.54 Crores, which is 44.8% of the anticipated cost of the projects.

4. Out of the 571 projects, 6 projects are ahead of schedule, 175 are on schedule, 258 projects are delayed, and 31 projects have been sanctioned without any commissioning schedule/date. Further, in case of 101 projects neither the year of commissioning nor the tentative gestation period of the projects have been reported but subsequently in some of the cases, the date of completion have been finalized. Out of 258 delayed projects, 75 projects had overall delay in the range of 1 to 12 months, 44 projects had a delay in the range of 13 to 24 months, 106 projects had a delay in the range of 25 to 60 months and 33 projects had a delay of 61 months and above.

5. It may be noted that this Ministry monitors the cost & time overrun with respect to original cost estimates (OCE) and not against the RCEs, as comparison against OCE reflect the actual changes. If the time and cost overruns is measured against the revised estimates, the calculated parameters will reflect only the unregularized RCEs due to which all time and cost overrun will get regularized resulting in zero value. This will not serve the purpose of monitoring.

6. The brief reasons for time overruns as reported by various projects implementing agencies are inadequate mobilization by the contractors, delay in land acquisitions, revision of scope of work, delay in supply of critical equipment, ROW problem, inadequate deployment of man power, contractual issues, delay in equipment erection and forest and environment clearances, etc.

7. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones drawn from the PERT Charts of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring.

8. The Sector-wise details of additional delays are as under:-

- i) In the **Shipping and Ports sector**, the project 'Setting up of LNG Regasification Terminal at Puthu Port Trust' has reported additional delay of 6 months due to shortage of

power and water supply and also due to evacuation of gas pipeline of GAIL at many places of Kerala State.

ii) In the **Telecommunications sector**, the project 'Project-III of NIB-II of Messaging Storage, BSNL' have reported additional delay of 1 month due to delay in delivery of equipment and non-readiness of BSNL sites .

iii) In the **Petroleum Sector**, 11 projects have reported additional delays in the range of 2-12 months. The project 'Construction of New Process Complex MHN, ONGC' has reported additional delay of 2 months due to delay in award of works, 'Offshore Grid Interconnectivity project in Mumbai High, ONGC' has reported additional delay of 2 months due to serious financial constraint, 'Karanpur Moradabad-Kashipur-Rudrapur Pipeline Project, GAIL' has reported additional delays of 2 months due to delay in construction work, 'Upgradation of Konaban GGS and Pipeline Grid Project, ONGC' has reported additional delay of 4 months due to poor progress of laying of pipeline works by the contractor, 'CDU/VDU-II, CPCL' and 'Compressor Stations (Kailaras & Chainsa), GAIL' have reported additional delay of 4 and 5 months respectively due to delay in delivery of critical equipment, 'Development of G-1 and GS-15, ONGC' has reported additional delay of 6 months due to contractual problems, 'Assam Renewal Project for Group-A, ONGC' has reported additional delay of 12 months due to Court cases and ROU issues, etc. Kochi-Kootanad Bangalore-Mangalore Pipeline project, GAIL' and 'Construction of 6 ETPs, ONGC have reported additional delay of 3 months each and 'Diesel Hydro Treator Project at Visakh Refinery, HPCL has reported additional delay of 6 months. However, no specific reasons have been reported by the project authorities for delay in these projects.

iv) In the **Power Sector**, 23 projects have reported additional delays in the range of 1-15 months. Three projects has reported additional delay of one month each, 3 projects have reported additional delay of two months each. 'Transmission system associated with Pallatana GBPP & BPT, PGCIL' has reported additional delay of 3 months due to delay in forest clearance. The projects '765 KV System for central part of Northern Grid, PGCIL', 'Northern Region System Strengthening Scheme-XV, PGCIL', 'Northern Region System Strengthening Scheme-XVIII, PGCIL', 'Northern Region System

Strengthening Scheme-XIX, PGCIL', have reported additional delay of 4 months, 6 months and 6 months respectively, and '765 KV System for Central part of Northern Grid Par, PGCIL' and Northern Region Transmission Strengthening Scheme, PGCIL' have reported additional delay of 7 months each. All these projects have reported delay due to delay in land acquisition. 'Eastern Region Strengthening Scheme-I, PGCIL' has reported additional delay of 7 months due to ROW problem, 'Bongaigaon Thermal Power Project, NTPC' has reported additional delay of 7 months due to delay in TG erection start 'Kameng HEP, NEEPCO' has reported additional delay of 9 months due to poor geological condition, 'Koldam HEP, NTPC' has reported additional delay of 12 months due to failure of right bank slope and seepage problem, 'Pare HEP, NEEPCO' has reported additional delay of 13 months due to poor geological condition and 'Barh STPP, Stage-I, NTPC' has reported additional delay of 15 months due to termination of contract and delay in retendering, 'Tapovan Visnugad HEP, NTPC' has reported additional delay of 15 months due to geological problem of power house service bay area. 'Barh STTP, Stage-II, NTPC' has reported additional delay of 5 months due to delay in supply of equipment. The project 'System Strengthening in NR for Sasan and Mundra, PGCIL' and '765 KV System for Central part of Northern Region, PGCIL' have reported additional delay of 4 months and 6 months respectively for which no reason have been reported by the project authority.

v) In **Steel sector**, 4 projects have reported additional delays in the range of 2-3 months. '67.5 MW TG-5 System Emergency Power Requirement, RINL', 'Expansion of Bhilai Steel Plant, SAIL' and 'Expansion of Durgapur Steel Plant, SAIL' have reported additional delays of 3 months each due to inadequate deployment of man power and increase in scope of work. The project 'Augmentation of Iron Ore Storage in RMHP, RINL' has reported additional delay of 2 months for which no reason has been reported by the project authority.

vi) In the **Road Transport and Highways Sector**, 6 projects of NHAI have reported additional delays in the range of 1-12 months. Four projects have reported additional delays of one month each, and one project has reported additional delay of two months and one project 'Panipat Jalandhar, 6 lanes, NHAI' has reported additional delay of 12 months. The project agency has not mentioned any specific reason for delay in these projects. However, general reasons for delay in these projects are delay in land

acquisition, forest & environment clearance, utility shifting problem, poor performance of contractor, etc.

vii) In the **Coal Sector**, 3 projects have been reported additional delays in the range of 24-36 months. The project 'Kulda OCP, Mahanadi Coal Fields' has reported additional delay of 24 months due to delay in land acquisition and R & R problem, 'Ananta OC expansion, Phase-III, MCL' has reported additional delay of 24 months due to delay in land acquisition, forest diversion and EMP clearances, 'Magahi OC Expansion Project, Singrauli, NCL has reported additional delay of 36 months due to delay in forest clearances and non-completion of Railway siding.

viii) In the **Railways Sector**, 5 projects have been reported additional delays in the range of 3-12 months. The project 'Tamluk Digha line doubling, SER' has reported additional delay of 12 months due to delay in land acquisition. 'Muzaffarpur Sitamarhi (NL), ECR' and 'Rajpipla-Ankelashwar, (GC), WR' have reported additional delay of 3 months each, 'Bandel-Naihali new Rail bridge in replacement of JER' has reported additional delay of 5 months and 'Freight Operations Information System, FOIS' has reported additional delay of 12 months. However, no specific reasons have been reported by the project authorities for delay in these projects.

9. The status as on 01.05.2012 in respect of projects costing ₹150 Crores and above in the various sectors is indicated in the Report.

(Pankaj Jain)
Special Secretary,
Min. of Statistics and Programme Implementation.

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Additional Delayed
1	Road Transport & Highways	148	6
2	Railways	131	5
3	Power	102	23
4	Petroleum	64	11
5	Coal	51	3
6	Shipping & Ports	22	1
7	Steel	16	4
8	Telecommunications	15	1
9	Fertilisers	6	0
10	Atomic Energy	5	0
11	Civil Aviation	5	0
12	Urban Development	4	0
13	Petrochemicals	1	0
14	Water Resources	1	0
	Total	571	54

ANNEXURE-I

Month wise List of Completed Project Costing Rs. 150 Crore and above during 2012-2013

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
April,2012				
<u>Power</u>				
1	KOTESHWAR HEP(THDC)(TEHRI HYDRO DEVELOPMENT CORPORATION LIMITED) - [180100184]	1,301.56	04/2005	2,635.39
2	WESTERN REGION STRENGTHENING SCHEME-X(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000049]	664.96	02/2012	362.10
<u>Road Transport & Highways</u>				
3	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000085]	600.24	10/2009	805.10
4	Bijapur-Hungund Section(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000137]	748.00	-	.00
<u>Shipping & Ports</u>				
5	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C(SHIPPING crp. of india) - [N25000033]	1,061.96	03/2012	1,284.15
6	ACQUISITION OF TWO NOS OF 120 B.P BY 077 & 078 (AH(SHIPPING crp. of india) - [N25000058]	241.50	09/2011	262.80
<u>Telecommunications</u>				
7	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G)(BHARAT SANCHAR NIGAM LIMITED) - [N26000046]	277.34	03/2009	308.13
8	GSM equipment of 1867000Lines (2G) 383000 lines 3((BHARAT SANCHAR NIGAM LIMITED) - [N26000089]	868.00	08/2009	558.78


Summary of projects in the Flash Report for the month of April, 2012

I. Project Implementation - Current Status:

Number of Projects in Previous Month	570
Number of Projects completed/dropped/frozen in Previous Month	15
Number of Projects completed/dropped/frozen in Current Month	8
Number of Projects are Removed in Current Month	1
Number of Projects Added in Current Month	25
Number of Projects in Current Month	571


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 571 projects, 6 projects are ahead of schedule, 175 projects are on schedule and 258 projects are delayed. Of the balance, 101 projects do not have fixed dates of commissioning while 31 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

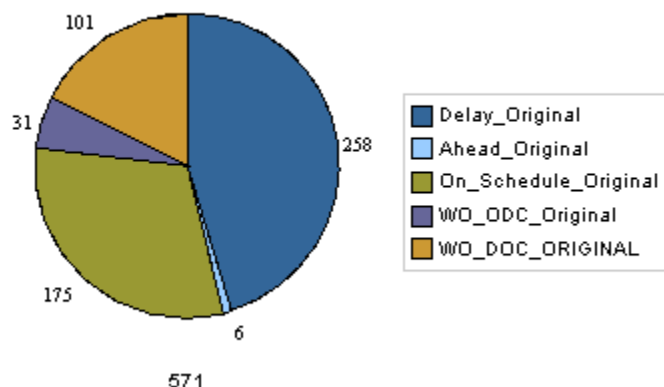

III. Investment Scenario

The Total Original cost of implementation of 571 projects when sanctioned, was of the order of Rs. 733514.85 crore but this was subsequently revised to Rs. 876715.9 crore implying a cost overrun of 19.5%. The expenditure incurred on these projects till April, 2012 is Rs. 392782.18 crore, which is 44.8% of the revised cost of the projects.

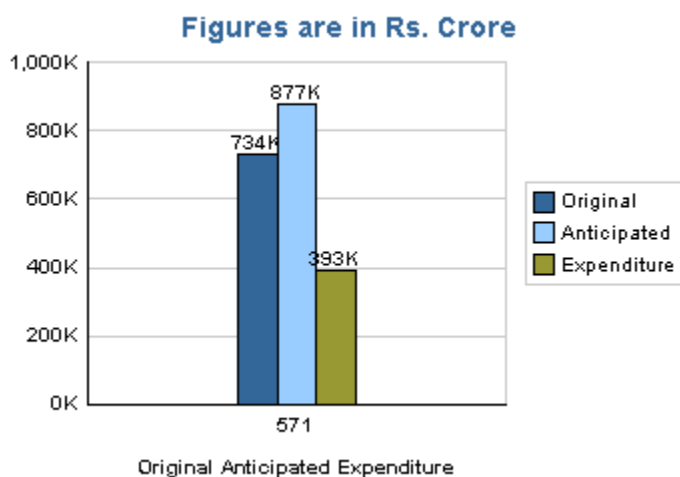

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	570
No of Projects Completed/Dropped/Frozen in Previous Month	15
No of Projects Completed/Dropped/Frozen in Current Month	8
No. of Projects Removed from the System	1
No of Projects added in Current Month	25
No of Projects in Current Month	571

II. Project status

With Respect To	Number of Projects						Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total	
Original (Date)	258	6	175	31	101	571	45.18
Latest Approved (Date)	255	4	239	36	37	571	44.66

III. (A) Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	446	590,358.16	648,892.75	257,337.49	39.70	58,534.59	9.90
Latest Approved (RCE)	125	203,194.16	227,823.15	135,269.05	59.40	24,628.99	12.10
Total (RCE)	571	793,552.32	876,715.90	392,606.54	44.78	83163.58	10.48
Original Cost of All Projects							
Original Cost	571	733,514.85	876,715.90	392,606.54	44.80	143,201.05	19.50

III. (B) Delayed Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	258	388,740.05	464,512.20	257,475.29	55.40	75,772.15	19.50
Latest Approved (RCE)	255	345,209.76	389,700.74	213,501.70	54.80	44,490.98	12.90

IV. Additional Delayed Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Latest Approved	56	85,180.70	106,272.16	68,865.74	64.80	21,091.46	24.80

Extent of cost overrun in projects with respect to original schedule(Sector Wise)

S.No.	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Original	Anticipated cost	Cost overrun (%)	No .	Original cost	Anticipated cost	% Incr Base
1	Atomic Energy	5	41,548.3	46,386.3	11.6	2	16,663.0	21,501.0	29.0
2	Civil Aviation	5	5,021.6	5,611.1	11.7	2	3,750.5	4,340.0	15.7
3	Coal	51	33,815.1	37,312.2	10.3	12	12,779.2	16,874.0	32.0
4	Fertilisers	6	5,317.4	5,317.4	0.0	0	0.0	0.0	0.0
5	Steel	16	50,155.8	71,402.4	42.4	8	32,529.9	53,806.4	65.4
6	Petrochemicals	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	63.4
7	Petroleum	64	155,278.0	164,778.9	6.1	16	52,549.6	69,449.1	32.2
8	Power	102	211,144.7	225,276.4	6.7	18	40,930.0	55,061.8	34.5
9	Railways	131	65,286.3	141,884.1	117.3	108	40,246.6	116,891.0	190.4
10	Road Transport & Highways	148	92,330.1	94,297.4	2.1	13	3,793.8	6,330.2	66.9
11	Shipping & Ports	22	17,207.9	18,722.9	8.8	10	8,732.5	10,579.5	21.2
12	Telecommunications	15	6,161.0	6,101.8	-1.0	2	1,065.9	1,089.3	2.2
13	Urban Development	4	44,245.2	49,518.1	11.9	2	6,509.2	11,782.1	81.0
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		571	733,514.9	876,715.9	19.5	195	225,553.7	377,811.5	67.5

Extent of cost overrun in projects with respect to original schedule(State Wise)

S.No.	State	No. of Projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Original	Anticipated cost	Cost overrun (%)	No .	Original cost	Anticipated cost	% Incr Base
1	Andhra Pradesh	36	31,031.6	38,459.0	23.9	14	12,420.0	20,714.4	66.8
2	Arunachal Pr.	4	9,512.2	14,153.6	48.8	2	6,441.3	11,082.7	72.1
3	Assam	37	23,895.8	35,736.3	49.6	13	11,923.7	23,858.3	100.1
4	Bihar	32	30,891.8	35,948.1	16.4	13	12,338.8	17,395.2	41.0
5	Goa	1	335.6	335.6	0.0	0	0.0	0.0	0.0
6	Gujarat	24	31,509.3	31,737.3	0.7	5	2,413.7	2,875.2	19.1
7	Haryana	10	5,795.4	7,611.8	31.3	3	1,448.2	3,264.7	125.4
8	Himachal Pr.	6	14,761.2	17,455.4	18.3	3	7,629.8	10,324.0	35.3
9	J and K	11	15,120.1	34,413.1	127.6	6	7,866.5	27,186.4	245.6
10	Karnataka	24	29,909.6	38,742.5	29.5	10	8,795.3	18,034.7	105.0
11	Kerala	5	5,469.7	6,911.2	26.4	3	4,295.7	5,737.2	33.6
12	Madhya pradesh	25	16,968.5	17,262.9	1.7	3	2,027.6	2,741.5	35.2
13	Maharashtra	50	78,548.3	93,760.5	19.4	18	31,818.4	49,505.1	55.6
14	Manipur	1	727.6	3,056.9	320.2	1	727.6	3,056.9	320.2
15	Meghalaya	2	762.0	762.0	0.0	0	0.0	0.0	0.0
16	Mizoram	3	1,901.7	4,220.8	121.9	2	988.1	3,307.1	234.7
17	Nagaland	1	850.0	850.0	0.0	0	0.0	0.0	0.0
18	Orissa	30	57,405.4	61,206.4	6.6	13	33,147.5	37,140.9	12.0
19	Punjab	6	4,384.2	5,314.2	21.2	2	532.4	1,462.5	174.7
20	Rajasthan	15	26,688.0	26,417.9	-1.0	4	1,224.0	1,624.4	32.7
21	Sikkim	2	1,648.9	3,690.0	123.8	1	1,339.5	3,380.6	152.4
22	Tamil Nadu	35	52,241.3	61,100.4	17.0	13	27,364.2	36,223.3	32.4
23	Tripura	3	1,522.4	2,053.2	34.9	2	1,234.4	1,765.2	43.0
24	Uttar Pradesh	25	18,779.7	22,785.2	21.3	9	3,729.2	7,783.0	108.7
25	West Bengal	26	40,460.8	52,785.0	30.5	16	21,201.4	33,525.6	58.1
26	Delhi	3	37,985.0	37,965.4	-0.1	0	0.0	0.0	0.0
27	Chhatisgarh	26	41,057.6	56,554.6	37.7	10	10,407.1	25,904.0	148.9
28	Jharkhandd	23	11,785.5	16,601.5	40.9	7	5,213.3	10,201.2	95.7
29	Uttaranchal	4	8,514.3	9,454.7	11.0	2	2,640.7	3,581.2	35.6
30	Multi State	101	133,051.5	139,370.1	4.7	20	6,385.4	16,136.2	152.7
Total		571	733,514.9	876,715.9	19.5	195	225,553.7	377,811.5	67.5

Extent of the time overrun in projects with respect to original schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.3	46,386.3	11.6	4	38,056.3	40,709.3	3 - 51
2	Civil Aviation	5	5,021.6	5,611.1	11.7	3	2,587.6	2,970.1	3 - 27
3	Coal	51	33,815.1	37,312.2	10.3	23	17,193.7	20,188.3	12 - 60
4	Fertilisers	6	5,317.4	5,317.4	0.0	2	763.0	763.0	9 - 12
5	Steel	16	50,155.8	71,402.4	42.4	7	13,065.8	17,149.7	3 - 36
6	Petrochemicals	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
7	Petroleum	64	155,278.0	164,778.9	6.1	40	109,624.7	119,448.9	1 - 120
8	Power	102	211,144.7	225,276.4	6.7	51	137,982.7	151,501.3	2 - 103
9	Railways	131	65,286.3	141,884.1	117.3	30	22,991.8	55,534.6	3 - 216
10	Road Transport & Highways	148	92,330.1	94,297.4	2.1	80	29,705.5	32,032.8	2 - 101
11	Shipping & Ports	22	17,207.9	18,722.9	8.8	9	7,833.4	9,411.1	8 - 93
12	Telecommunications	15	6,161.0	6,101.8	-1.0	7	1,997.6	2,007.1	21 - 77
13	Urban Development	4	44,245.2	49,518.1	11.9	1	6,395.0	11,609.0	24 - 24
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	60 - 60
Total		571	733,514.9	876,715.9	19.5	258	388,740.1	464,512.2	

Extent of the time overrun in projects with respect to original schedule(State Wise)

S. No	State	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Andhra Pradesh	36	31,031.6	38,459.0	23.9	11	16,104.8	19,607.3	4 - 36
2	Arunachal Pr.	4	9,512.2	14,153.6	48.8	3	9,356.2	13,737.9	25 - 63
3	Assam	37	23,895.8	35,736.3	49.6	31	11,648.4	19,587.3	12 - 120
4	Bihar	32	30,891.8	35,948.1	16.4	14	24,110.8	26,414.8	2 - 75
5	Goa	1	335.6	335.6	0.0	1	335.6	335.6	3 - 3
6	Gujarat	24	31,509.3	31,737.3	0.7	6	13,912.3	14,143.8	3 - 24
7	Haryana	10	5,795.4	7,611.8	31.3	4	2,065.9	3,555.1	9 - 50
8	Himachal Pr.	6	14,761.2	17,455.4	18.3	6	14,761.2	17,455.4	20 - 59
9	J and K	11	15,120.1	34,413.1	127.6	8	9,873.4	29,166.4	10 - 201
10	Karnataka	24	29,909.6	38,742.5	29.5	6	19,921.5	24,895.5	9 - 94
11	Kerala	5	5,469.7	6,911.2	26.4	3	4,674.0	5,324.0	8 - 27
12	Madhya pradesh	25	16,968.5	17,262.9	1.7	16	12,531.8	12,112.4	5 - 50
13	Maharashtra	50	78,548.3	93,760.5	19.4	20	45,959.1	56,032.9	7 - 52
14	Manipur	1	727.6	3,056.9	320.2	1	727.6	3,056.9	60 - 60
15	Meghalaya	2	762.0	762.0	0.0	0	0.0	0.0	-
16	Mizoram	3	1,901.7	4,220.8	121.9	1	368.7	913.6	103 - 103
17	Nagaland	1	850.0	850.0	0.0	0	0.0	0.0	-
18	Orissa	30	57,405.4	61,206.4	6.6	9	31,475.9	32,310.2	7 - 101
19	Punjab	6	4,384.2	5,314.2	21.2	3	1,362.9	1,437.9	7 - 51
20	Rajasthan	15	26,688.0	26,417.9	-1.0	5	19,197.2	18,892.9	3 - 47
21	Sikkim	2	1,648.9	3,690.0	123.8	1	309.5	309.5	27 - 27
22	Tamil Nadu	35	52,241.3	61,100.4	17.0	8	22,346.7	26,451.5	16 - 93
23	Tripura	3	1,522.4	2,053.2	34.9	1	288.0	288.0	4 - 4
24	Uttar Pradesh	25	18,779.7	22,785.2	21.3	13	11,442.4	13,374.4	5 - 87
25	West Bengal	26	40,460.8	52,785.0	30.5	16	13,209.4	18,399.5	3 - 132
26	Delhi	3	37,985.0	37,965.4	-0.1	0	0.0	0.0	-
27	Chhatisgarh	26	41,057.6	56,554.6	37.7	7	12,442.3	14,436.8	10 - 48
28	Jharkhandd	23	11,785.5	16,601.5	40.9	8	2,258.6	2,702.4	24 - 102
29	Uttaranchal	4	8,514.3	9,454.7	11.0	4	8,514.3	9,454.7	13 - 36
30	Multi State	101	133,051.5	139,370.1	4.7	52	79,541.6	80,115.4	1 - 216
Total		571	733,514.9	876,715.9	19.5	258	388,740.1	464,512.2	

Extent of the time overrun in projects with respect to latest schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.3	46,386.3	11.6	5	41,548.3	46,386.3	3 - 51
2	Civil Aviation	5	5,021.6	5,611.1	11.7	2	2,278.1	2,660.6	3 - 17
3	Coal	51	33,815.1	37,312.2	10.3	21	15,095.7	18,509.7	12 - 60
4	Fertilisers	6	5,317.4	5,317.4	0.0	2	763.0	763.0	9 - 12
5	Steel	16	50,155.8	71,402.4	42.4	6	4,373.8	4,858.7	3 - 22
6	Petrochemicals	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
7	Petroleum	64	155,278.0	164,778.9	6.1	33	65,955.0	72,079.5	1 - 80
8	Power	102	211,144.7	225,276.4	6.7	48	127,879.0	138,471.3	2 - 103
9	Railways	131	65,286.3	141,884.1	117.3	37	15,925.5	51,386.7	0 - 216
10	Road Transport & Highways	148	92,330.1	94,297.4	2.1	80	29,705.5	32,032.8	2 - 101
11	Shipping & Ports	22	17,207.9	18,722.9	8.8	7	4,011.2	5,052.3	14 - 93
12	Telecommunications	15	6,161.0	6,101.8	-1.0	12	4,700.0	4,703.8	7 - 77
13	Urban Development	4	44,245.2	49,518.1	11.9	1	6,395.0	11,609.0	24 - 24
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	60 - 60
Total		571	733,514.9	876,715.9	19.5	255	319,172.9	389,700.7	

Extent of cost overrun in projects with respect to latest schedule

S.No.	Sector	No. of projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Latest approved	Anticipated cost	Cost overrun (%)	No .	Latest approved	Anticipated cost	% Increase Base
1	Atomic Energy	5	41,548.3	46,386.3	11.6	2	16,663.0	21,501.0	29.0
2	Civil Aviation	5	5,228.6	5,611.1	7.3	1	1,942.5	2,325.0	19.7
3	Coal	51	35,022.7	37,312.2	6.5	8	5,161.8	7,451.2	44.4
4	Fertilisers	6	5,317.4	5,317.4	0.0	0	0.0	0.0	0.0
5	Steel	16	56,031.1	71,402.4	27.4	5	9,099.0	24,500.3	169.3
6	Petrochemicals	1	8,920.0	8,920.0	0.0	0	0.0	0.0	0.0
7	Petroleum	64	169,294.5	164,778.9	-2.7	3	32,179.4	33,014.1	2.6
8	Power	102	215,028.0	225,276.4	4.8	13	35,648.2	45,896.7	28.7
9	Railways	131	95,083.9	141,884.1	49.2	82	49,246.9	96,256.2	95.5
10	Road Transport & Highways	148	92,496.6	94,297.4	1.9	12	3,597.3	5,967.2	65.9
11	Shipping & Ports	22	18,569.4	18,722.9	0.8	7	4,306.6	4,770.0	10.8
12	Telecommunications	15	6,164.9	6,101.8	-1.0	0	0.0	0.0	0.0
13	Urban Development	4	44,304.1	49,518.1	11.8	1	6,395.0	11,609.0	81.5
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		571	793,552.3	876,715.9	10.5	135	164,782.5	254,477.7	54.4

Extent of time & cost overrun in projects with respect to latest schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.29	46,386.29	11.64	0	0.00	0.00	0- 0
2	Civil Aviation	5	5,021.58	5,611.07	11.74	1	1,808.00	2,015.00	13- 13
3	Coal	51	33,815.11	37,312.15	10.34	1	469.78	706.40	44- 44
4	Fertilisers	6	5,317.41	5,317.41	0.00	0	0.00	0.00	0- 0
5	Steel	16	50,155.82	71,402.36	42.36	2	8,987.89	12,898.17	10- 36
6	Petrochemicals	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
7	Petroleum	64	155,277.97	164,778.94	6.12	13	21,195.88	36,044.22	6- 120
8	Power	102	211,144.68	225,276.41	6.69	3	2,622.17	4,899.65	24- 103
9	Railways	131	65,286.30	141,884.10	117.33	11	4,300.85	13,899.44	2- 141
10	Road Transport & Highways	148	92,330.10	94,297.43	2.13	0	0.00	0.00	0- 0
11	Shipping & Ports	22	17,207.90	18,722.87	8.80	3	4,022.70	4,800.25	8- 22
12	Telecommunications	15	6,161.00	6,101.79	-0.96	0	0.00	0.00	0- 0
13	Urban Development	4	44,245.18	49,518.08	11.92	0	0.00	0.00	0- 0
14	Water Resources	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		571	733514.85	876715.9	19.52	34	43407.27	75263.13	

Extent of time & cost overrun in projects with respect to original schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.29	46,386.29	11.64	1	13,171.00	15,824.00	51- 51
2	Civil Aviation	5	5,021.58	5,611.07	11.74	1	1,942.51	2,325.00	17- 17
3	Coal	51	33,815.11	37,312.15	10.34	7	10,603.60	14,195.94	19- 48
4	Fertilisers	6	5,317.41	5,317.41	0.00	0	0.00	0.00	0- 0
5	Steel	16	50,155.82	71,402.36	42.36	4	9,477.89	13,591.75	10- 36
6	Petrochemicals	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
7	Petroleum	64	155,277.97	164,778.94	6.12	12	49,312.67	64,735.01	7- 120
8	Power	102	211,144.68	225,276.41	6.69	15	38,255.56	50,452.29	7- 103
9	Railways	131	65,286.30	141,884.10	117.33	21	11,114.96	43,587.82	3- 216
10	Road Transport & Highways	148	92,330.10	94,297.43	2.13	13	3,793.78	6,330.20	12- 99
11	Shipping & Ports	22	17,207.90	18,722.87	8.80	6	6,752.85	8,330.50	8- 93
12	Telecommunications	15	6,161.00	6,101.79	-0.96	1	149.15	158.72	36- 36
13	Urban Development	4	44,245.18	49,518.08	11.92	1	6,395.00	11,609.00	24- 24
14	Water Resources	1	542.90	1,187.00	118.64	1	542.90	1,187.00	60- 60
Total		571	733514.85	876715.9	19.52	83	151511.87	232327.23	

V. List of projects completed/dropped/Frozen current month

(All Cost /Expenditure in Rs. crore)

S.no	Project	DOA	Original		Now anticipated		Final Expenditure
			Cost	DOC	Cost	DOC	
	<u>Power</u>						
1	WESTERN REGION STRENGTHENING SCHEME-X	02/2009	664.96	02/2012	664.96	03/2012	362.10
2	KOTESHWAR HEP(THDC)	04/2000	1,301.56	04/2005	2,283.68	03/2012	2,635.39
	<u>Road Transport & Highways</u>						
3	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID	12/2003	600.24	10/2009	600.24	06/2012	805.10
4	Bijapur-Hungund Section	09/2010	748.00	N.A.	748.00	03/2013	.00
	<u>Shipping & Ports</u>						
5	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C	11/2007	1,061.96	03/2012	1,082.06	04/2012	1,284.15
6	ACQUISITION OF TWO NOS OF 120 B.P BY 077 & 078 (AH)	12/2010	241.50	09/2011	241.50	04/2012	262.80
	<u>Telecommunications</u>						
7	GSM equipment of 1867000Lines (2G) 383000 lines 3G	08/2008	868.00	08/2009	868.00	06/2012	558.78
8	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G)	11/2007	277.34	03/2009	377.54	04/2012	308.13

VI. List of projects added

(All Cost in Rs. crore)

S.no	Project	DOA	Original		Anticipated	
			Cost	DOC	Cost	DOC
	<u>Coal</u>					
1	BAROUD OC EXPANSION (RCE)- 3MTY	4/2012	258.56	3/2016	258.56	3/2016
	<u>Petroleum</u>					
2	Integrated Development of B-127 fields	12/2011	2,059.63	3/2015	2,059.63	3/2015
3	Heera and South Heera Redevelopment Ph-II	3/2012	5,608.40	5/2015	5,608.40	5/2015
4	Development of C-26 Cluster Fields	3/2012	2,592.17	5/2014	2,592.17	3/2015
	<u>Power</u>					
5	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS	12/2011	901.77	8/2014	901.77	8/2014
6	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-	2/2012	3,201.44	10/2014	3,201.44	10/2014
7	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV	11/2011	723.63	11/2014	723.63	11/2014
	<u>Road Transport & Highways</u>					
8	SNG toBANL	6/2011	1,100.70	6/2014	1,100.70	-
9	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER	11/2011	909.00	5/2014	909.00	5/2014
10	six laning of Chandikhol-Jagatpur-Bhubaneswar	12/2011	1,047.00	6/2014	1,047.00	6/2014
11	4-laning of Raiganj-Dalkola	2/2011	580.43	8/2013	580.43	8/2013
12	4-laning of Brahampore-Faraka	2/2011	998.79	8/2013	998.79	8/2013
13	4-laning of Faraka-Raiganj	2/2011	1,078.84	8/2013	1,078.84	8/2013
14	MUZAFFARNAGAR-HARIDWAR	9/2011	754.00	3/2013	754.00	3/2013
15	BAREILY-SITAPUR	3/2011	1,046.00	9/2013	1,046.00	9/2013
16	BEAWAR-PALI-PINDWARA	12/2011	2,388.00	6/2014	2,388.00	6/2014
17	JAIPUR-REENGUS	8/2010	267.81	2/2013	267.81	2/2013
18	PANIKHOLI-RIMOLI	3/2012	1,410.00	9/2014	1,410.00	9/2014
19	BHUBANESWAR TO PURI	3/2011	500.29	8/2013	500.29	8/2013
20	2laning with PS Gopalganj-Chappra	12/2011	325.00	5/2014	325.00	5/2014
21	BHOPAL-SANCHI	10/2011	209.00	1/2013	209.00	1/2013
22	PUNE-SHOLAPUR,Pkg-II	9/2011	835.00	1/2014	835.00	1/2014
23	NIROLI-ROXY-RAJAMUNDA	7/2011	586.00	1/2014	586.00	1/2014
24	4-laning of Barhi-Hazaribagh	2/2012	398.00	2/2014	398.00	2/2014
	<u>Telecommunications</u>					
25	NIB Project Capacity Expansion	6/2007	175.52	12/2008	175.52	5/2012

VII. Milestones (Cumulative due & achieved)

Total	2494
Achieved up to month	1118

VIII. List of projects reporting additional delays (Apr,2012)

S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>Coal</u>						
1	KULDA OCP (MAHANADI COALFIELDS LTD) MCL	302.96	302.96	03/2010	03/2012	03/2014	24
2	ANANTA OC EXPANSION PH-III 15.0 Mty MCL	207.28	207.28	03/2012	03/2012	03/2014	24
3	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI NCL	259.40	259.40	03/2012	03/2012	03/2015	36
	<u>Steel</u>						
4	Augmentation of Iron Ore Storage in RMHP RINL	480.00	450.00	05/2012	12/2012	02/2013	2
5	EXPANSION OF BHILAI STEEL PLANT SAIL	5,185.00	17,265.00	N.A.	06/2013	09/2013	3
6	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM RINL	230.00	343.58	02/2011	04/2012	07/2012	3
7	EXPANSION OF DURGAPUR STEEL PLANT SAIL	2,875.00	2,875.00	12/2012	12/2012	03/2013	3
	<u>Petroleum</u>						
8	CONSTRUCTION OF NEW PROCESS COMPLEX MHN ONGC	2,853.29	6,326.40	05/2010	05/2012	07/2012	2
9	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH ONGC	740.02	740.02	03/2010	03/2013	05/2013	2
10	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-GAIL	238.68	204.00	01/2012	05/2012	07/2012	2
11	KOCHI-KOOTANAD BANGALORE-MANGALORE PIPELINE PROJEC GAIL	348.00	261.00	03/2012	05/2012	08/2012	3
12	Construction of 6 ETPs ONGC	302.26	302.26	09/2012	09/2012	12/2012	3
13	Up-gradation of Konaban GGS and Pipeline Grid Project ONGC	288.04	288.04	08/2012	08/2012	12/2012	4
14	CDU/VDU-II CPCL	333.99	333.99	N.A.	05/2012	09/2012	4
15	COMPRESSOR STATIONS (KAILARAS AND CHAINSA) GAIL	1,167.00	798.00	04/2011	04/2012	09/2012	5
16	DEV OF G1 AND GS-15 (ONGCL) ONGC	429.82	2,735.65	04/2006	06/2012	12/2012	6

VIII. List of projects reporting additional delays (Apr,2012)


S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
17	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY HPCL	3,597.00	2,730.00	09/2011	03/2012	09/2012	6
18	ASSAM RENEWAL PROJECT FOR GROUP A ONGC	2,465.15	2,378.86	03/2013	03/2013	03/2014	12
Power							
19	SIPAT STPP STAGE - I (NTPC) NTPC	8,323.39	8,323.39	12/2009	04/2012	05/2012	1
20	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION PGCIL	196.10	196.10	07/2011	05/2012	06/2012	1
21	MAUDA TRANSMISSION SYSTEM PGCIL	469.38	469.38	10/2012	04/2012	05/2012	1
22	CHAMERA,STAGE-III (NHPC) NHPC	1,405.63	2,084.00	08/2010	04/2012	06/2012	2
23	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP PGCIL	557.24	557.24	01/2010	12/2012	02/2013	2
24	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI PGCIL	1,677.57	1,677.57	04/2013	04/2013	06/2013	2
25	Trans. System associated with PALLATANA GBPP & BPT PGCIL	2,144.00	2,144.00	12/2012	12/2012	03/2013	3
26	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA PGCIL	1,347.32	1,347.32	02/2012	06/2012	10/2012	4
27	System Strengthening in NR for SASAN & MUNDRA (UMPP) PGCIL	1,216.83	1,216.83	08/2012	08/2012	12/2012	4
28	BARH STPP STAGE -II NTPC	7,341.04	7,341.04	08/2013	01/2014	06/2014	5
29	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV PGCIL	520.48	520.48	11/2011	12/2012	06/2013	6
30	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII PGCIL	509.66	509.66	11/2011	12/2012	06/2013	6
31	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX PGCIL	410.29	410.29	02/2012	12/2012	06/2013	6
32	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G PGCIL	1,736.36	1,736.36	06/2012	06/2012	12/2012	6
33	EASTERN REGION STRENGTHENING SCHEME-I PGCIL	975.96	975.96	10/2009	05/2012	12/2012	7
34	BONGAIGAON THERMAL POWER PROJECT NTPC	4,375.35	4,375.35	N.A.	04/2014	11/2014	7
35	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR PGCIL	1,075.12	1,075.12	05/2012	05/2012	12/2012	7
36	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME PGCIL	965.58	965.58	11/2012	11/2012	06/2013	7
37	KAMENG HYDROELECTRIC PROJECT (NEEPCO) NEEPCO	2,496.90	2,496.90	05/2013	06/2016	03/2017	9
38	KOLDAM HEP (NTPC) NTPC	4,527.15	4,527.15	04/2009	03/2013	03/2014	12
39	PARE HYDRO ELECTRIC PROJECT(110 MW) NEEPCO	573.99	573.99	08/2012	08/2013	09/2014	13
40	BARH STPP STAGE I (3X660MW) NTPC NTPC	8,692.97	8,693.00	12/2009	12/2014	03/2016	15
41	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) NTPC	2,978.48	2,978.48	03/2013	06/2014	09/2015	15

Railways


VIII. List of projects reporting additional delays (Apr,2012)

S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
42	MUZAFFARPUR-SITAMARHI(NL), ECR ECR	100.00	484.03	03/2012	03/2012	06/2012	3
43	RAJPIPLA-ANKELASHWAR, WR (GC) WR	196.97	196.97	03/2011	03/2012	06/2012	3
44	Bandel-Naihati new rail bridge in replacement of j ER	207.52	207.52	12/2012	12/2012	05/2013	5
45	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) FOIS	520.00	634.13	03/1995	03/2012	03/2013	12
46	TAMLUK DIGHA, LINE DOUBLING (SER) SER	293.97	1,086.41	06/2005	06/2015	06/2016	12
<u>Road Transport & Highways</u>							
47	HALDIA PORT (PORT CONNECTIVITY) (NH-41) NHAI	273.00	522.00	03/2005	04/2012	05/2012	1
48	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) NHAI	227.00	227.00	12/2008	04/2012	05/2012	1
49	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) NHAI	225.00	225.00	10/2008	04/2012	05/2012	1
50	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI NHAI	441.00	441.00	N.A.	04/2012	05/2012	1
51	Armur to kadloor yellareddy NHAI	390.56	390.56	02/2012	04/2012	06/2012	2
52	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) NHAI	1,108.00	2,288.00	11/2011	06/2012	06/2013	12
<u>Shipping & Ports</u>							
53	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU PORT TRUST	3,500.00	4,150.00	01/2012	03/2012	09/2012	6
<u>Telecommunications</u>							
54	PROJ.III OF NIB-II OF MESSAGING STORAGE BSNL	250.00	250.00	12/2005	04/2012	05/2012	1

Trend and Graphical Analysis of All Projects

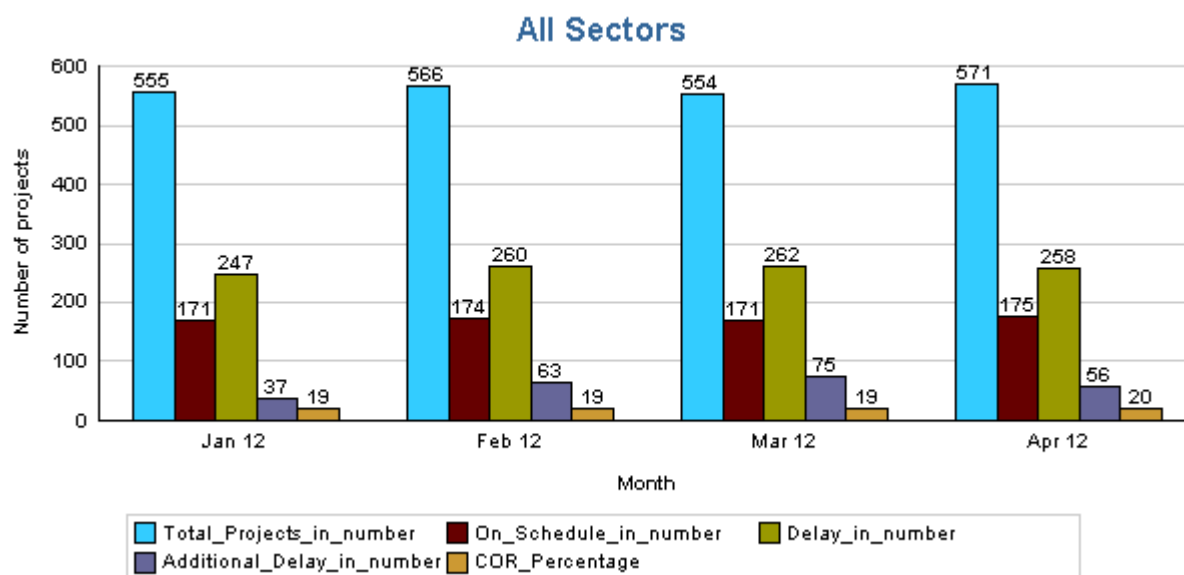


All Sectors Break-up of 258 Delayed projects in April 2012

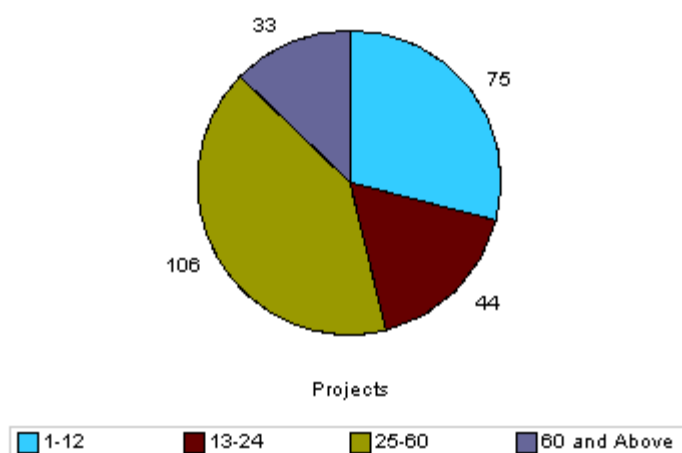


Trend and Graphical Analysis

Urban Development Sector

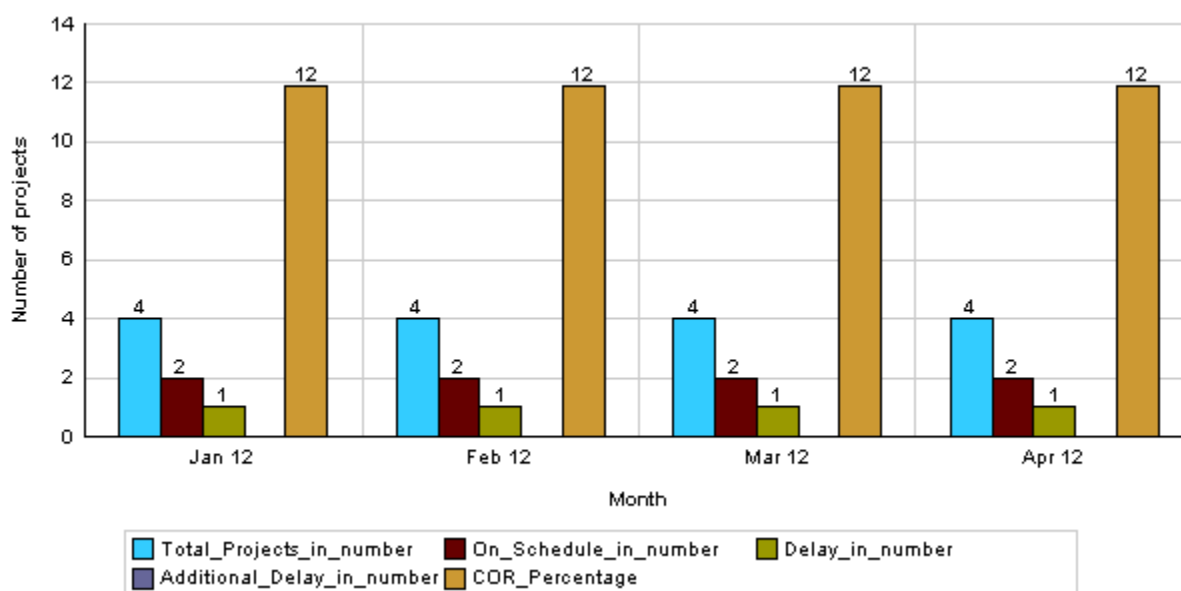


Urban Development Sector Break-up of 1 Delayed projects in April 2012




Trend and Graphical Analysis


Telecommunications Sector

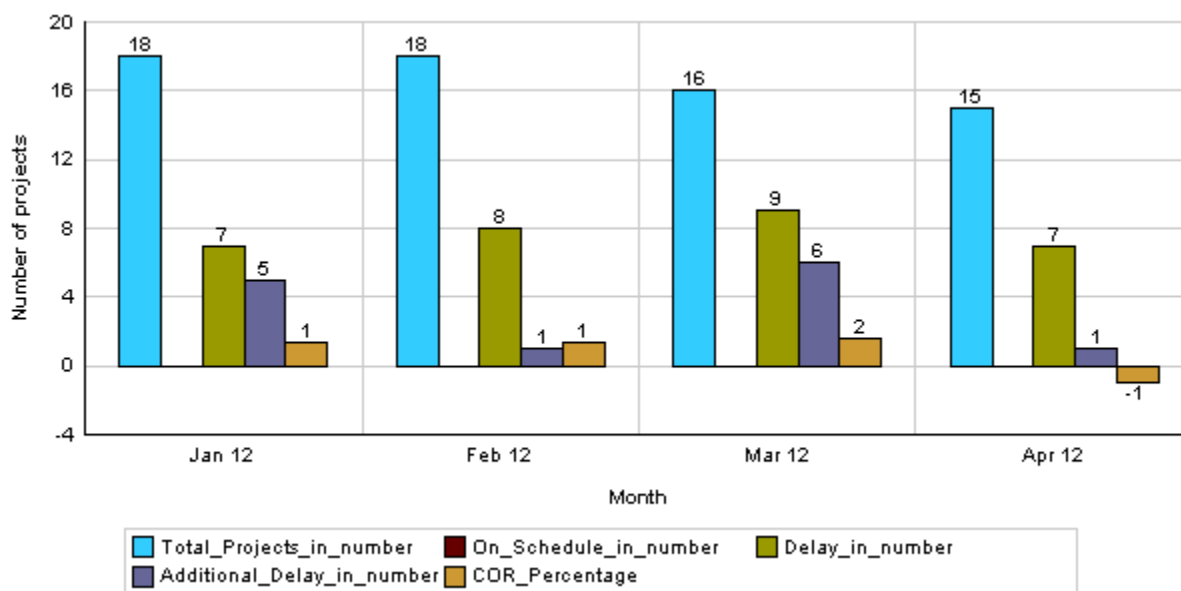


Telecommunications Sector Break-up of 7 Delayed projects in April 2012

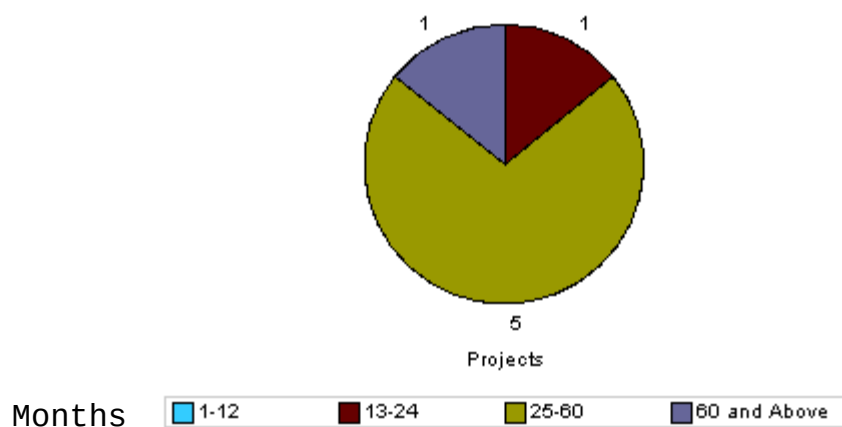


Trend and Graphical Analysis Shipping and Ports Sector

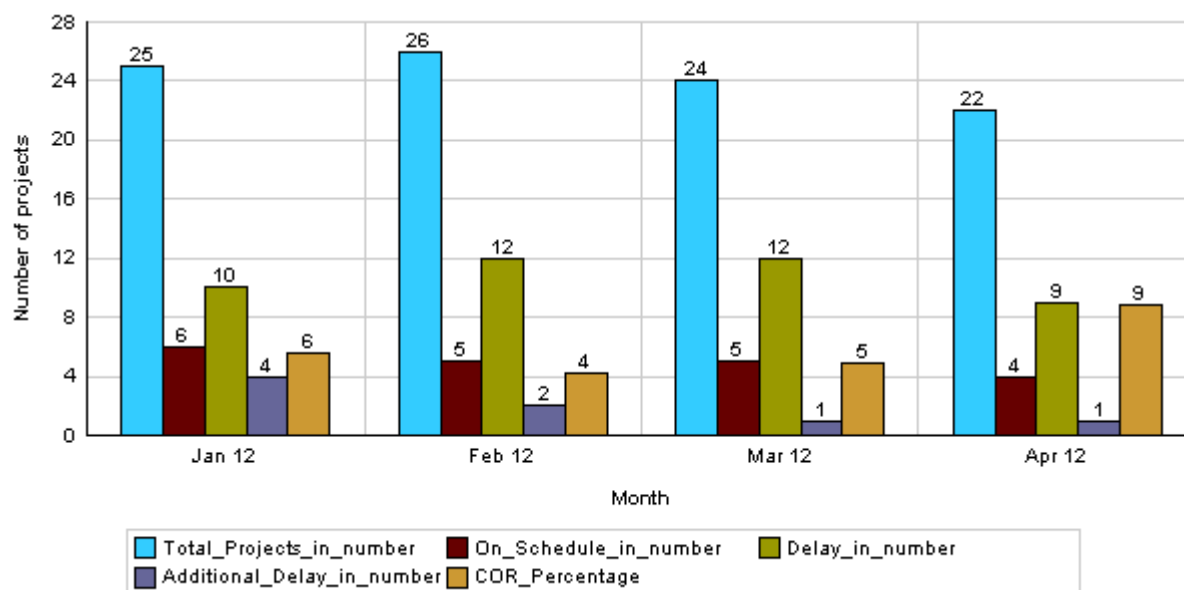


Sector Break-up of 9 Delayed projects in April 2012

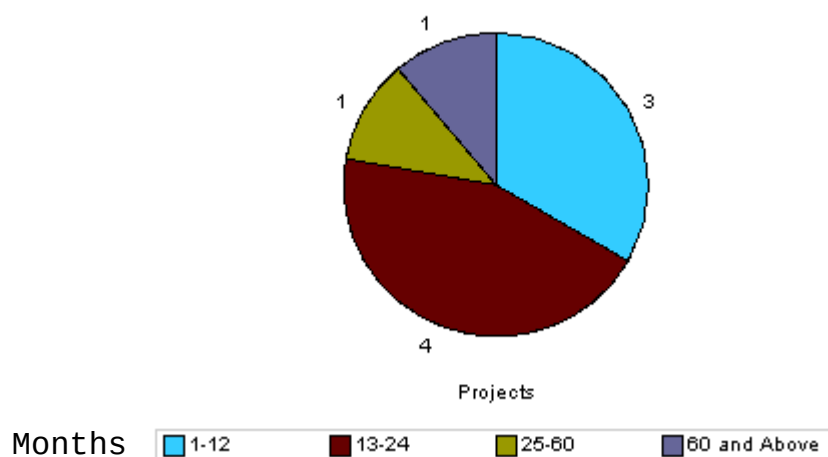

Trend and Graphical Analysis Road Transport and Highways Sector

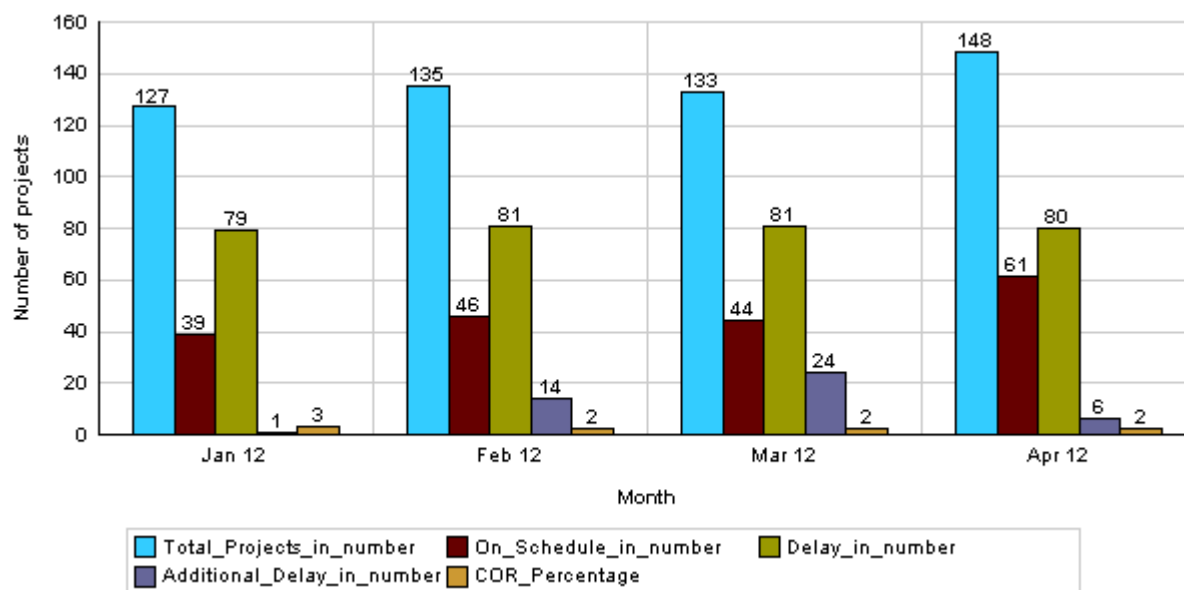


Sector Break-up of 80 Delayed projects in April 2012

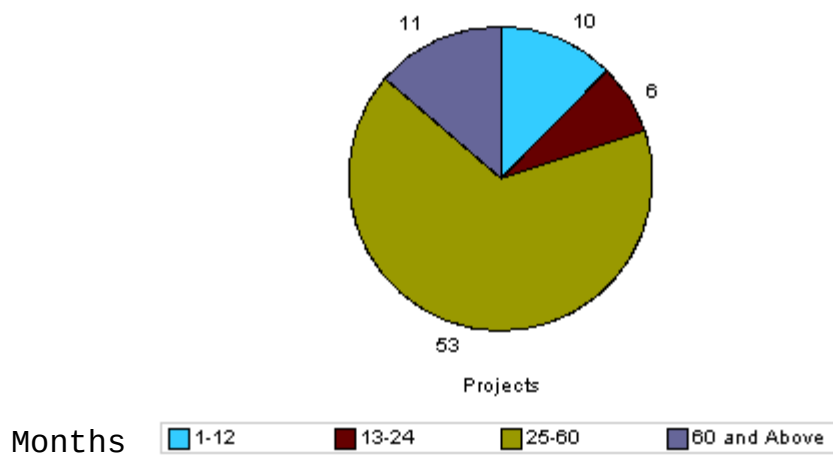


Trend and Graphical Analysis

Railways Sector

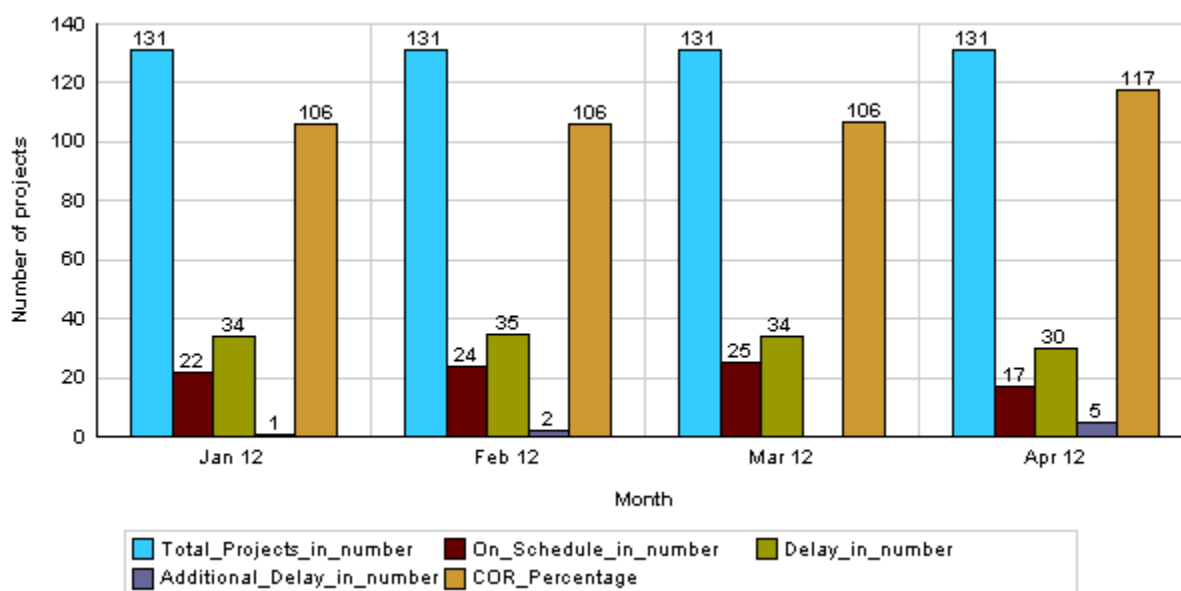


Railways Sector Sector Break-up of 30 Delayed projects in April 2012

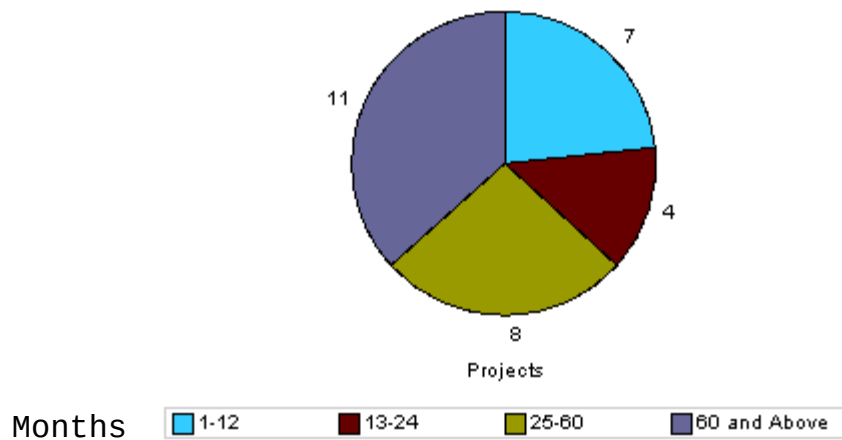


Trend and Graphical Analysis

Power Sector

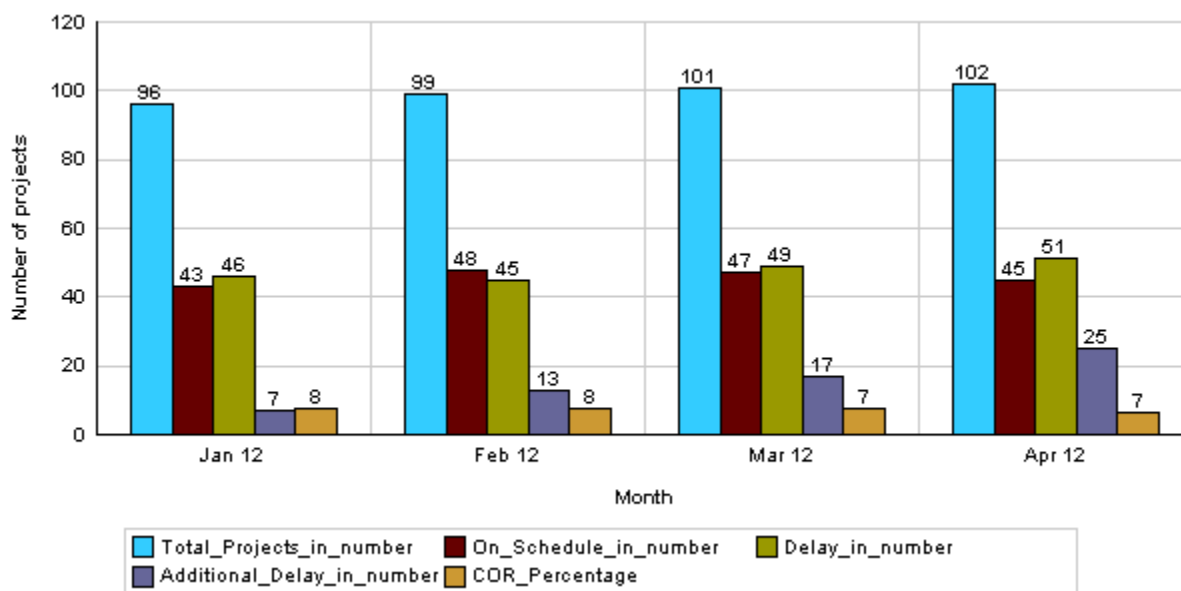


Power Sector Sector Break-up of 51 Delayed projects in April 2012

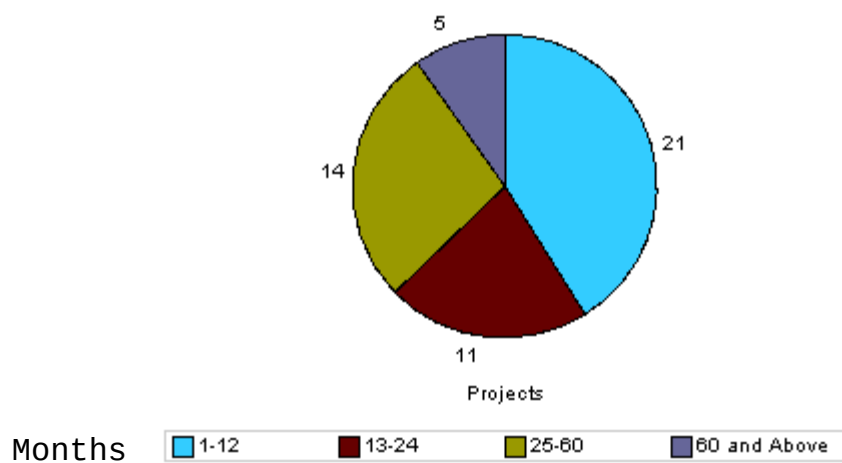


Trend and Graphical Analysis

Petroleum Sector

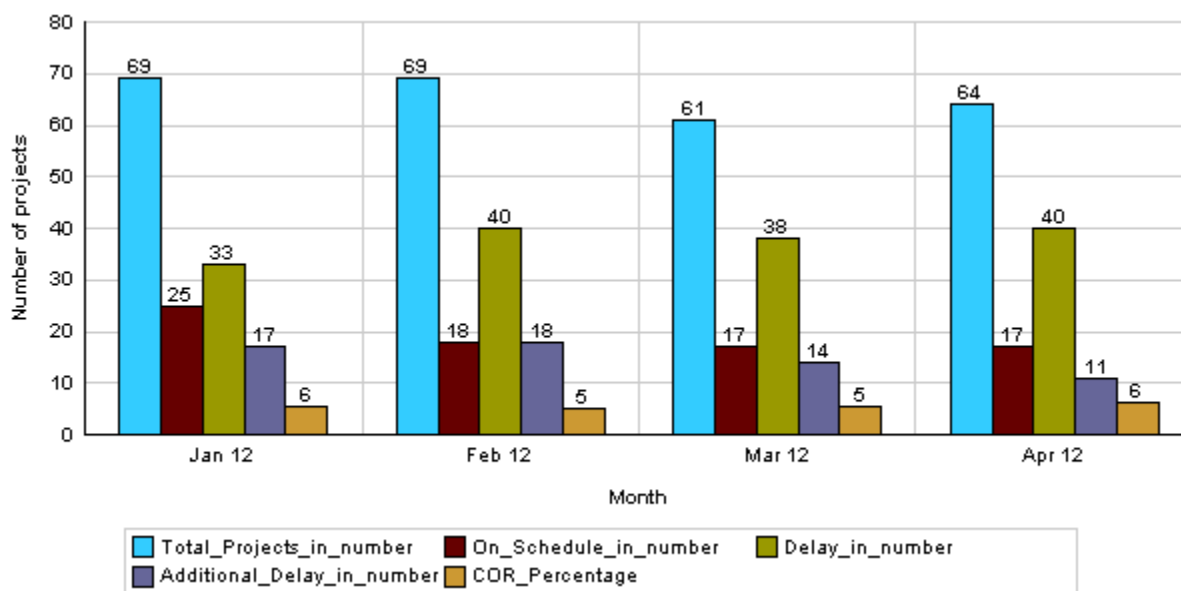


Petroleum Sector Sector Break-up of 40 Delayed projects in April 2012


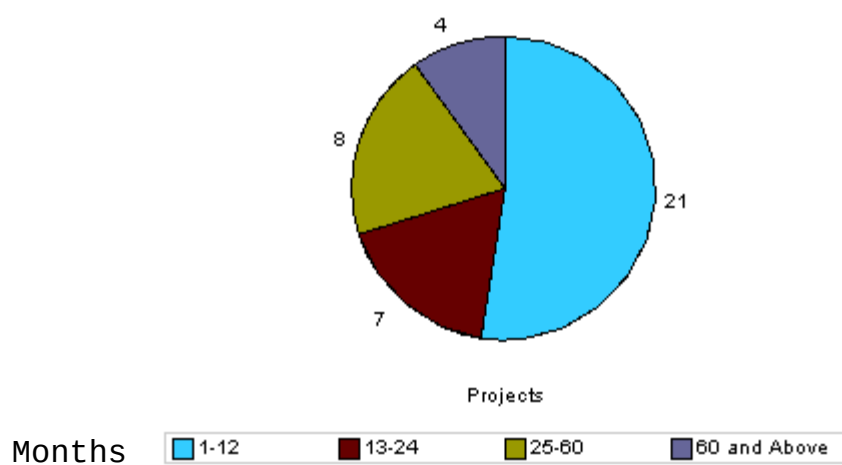


Trend and Graphical Analysis

Steel Sector

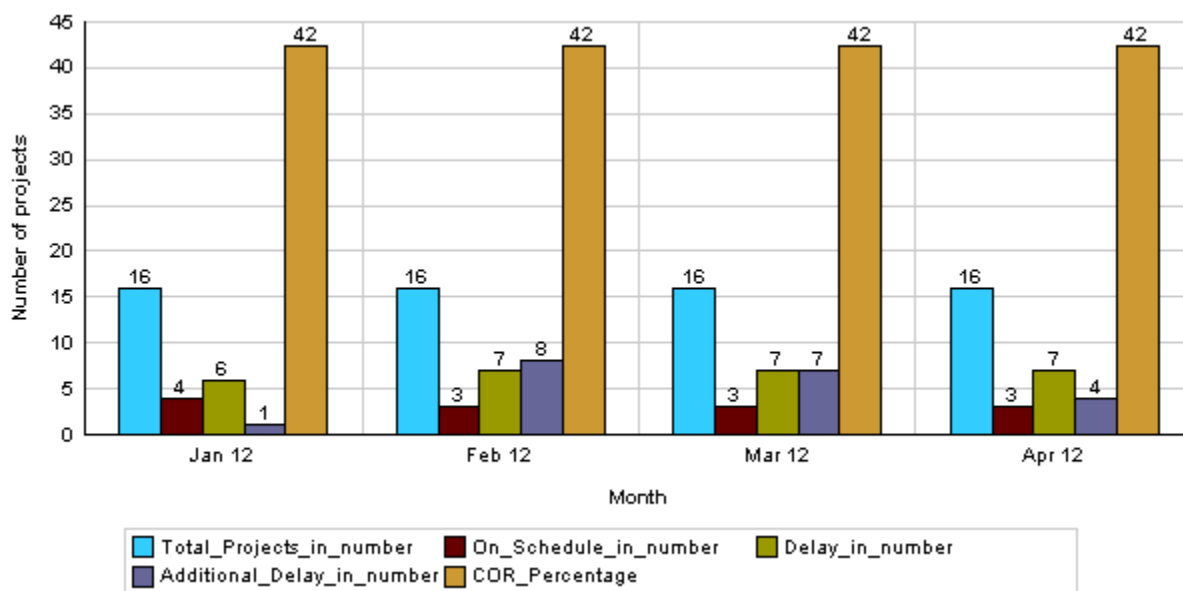


Steel Sector Break-up of 7 Delayed projects in April 2012

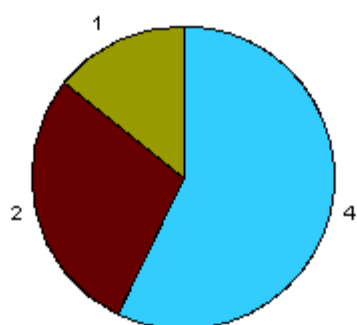


Trend and Graphical Analysis

Fertilisers Sector

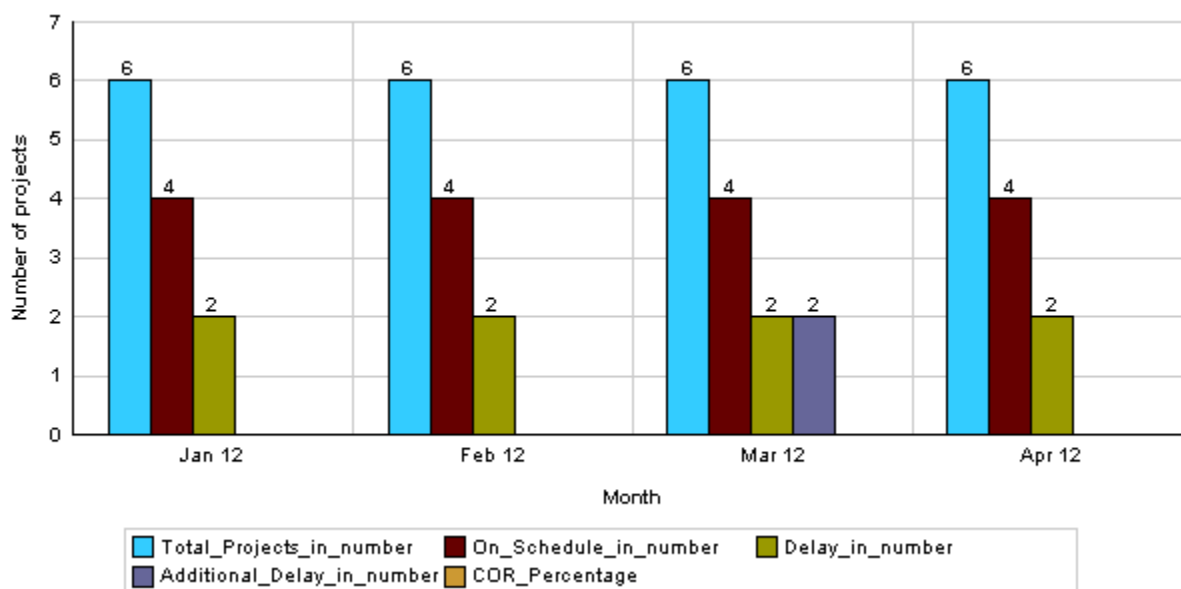


Fertilisers Sector Sector Break-up of 2 Delayed projects in April 2012

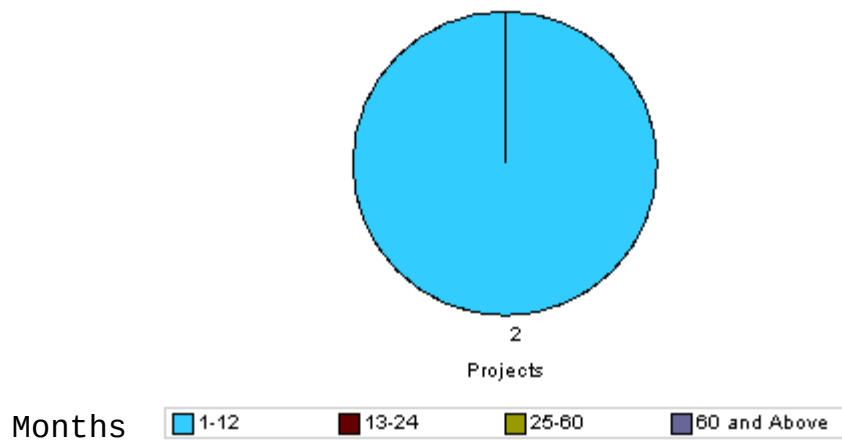


Trend and Graphical Analysis

Coal Sector

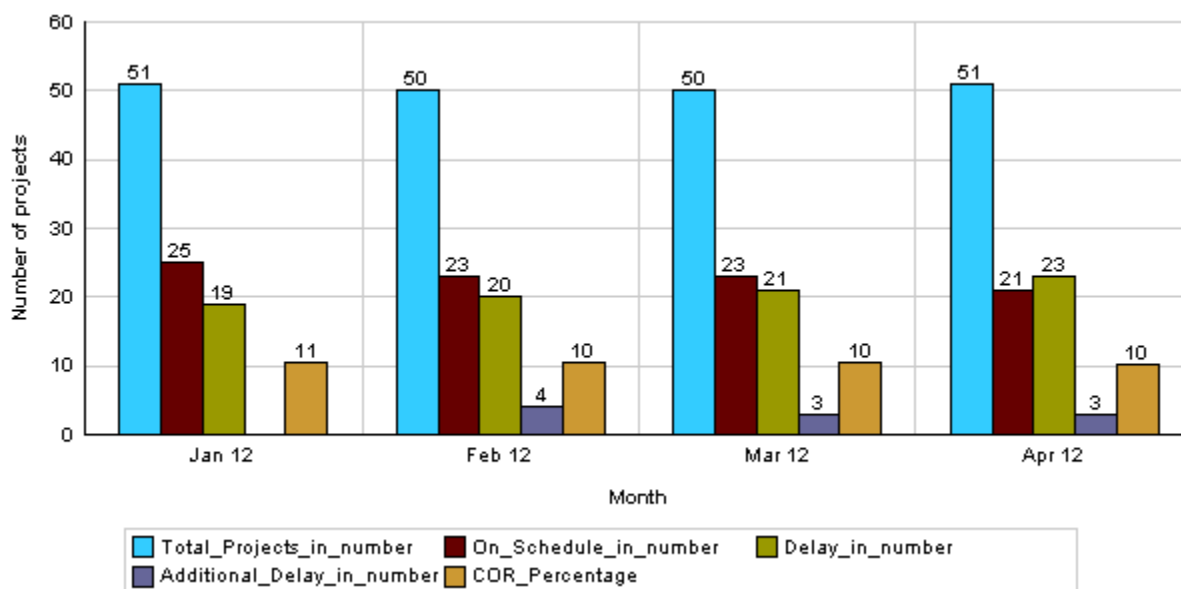


Coal Sector Sector Break-up of 23 Delayed projects in April 2012

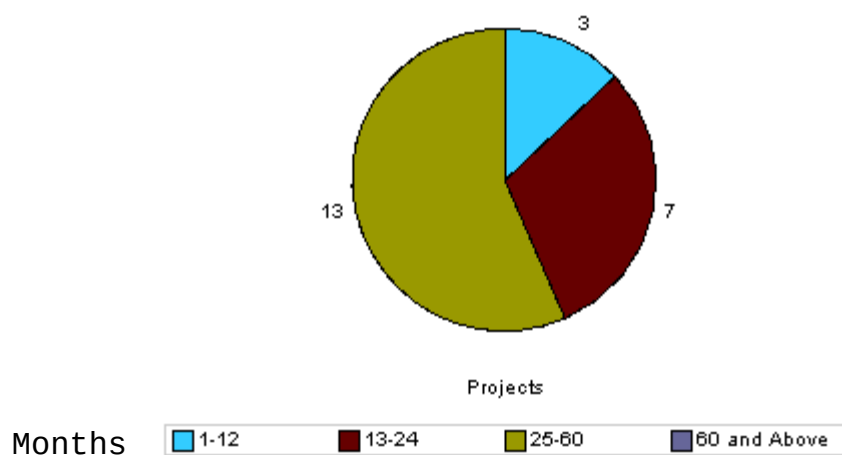


Trend and Graphical Analysis

Civil Aviation Sector

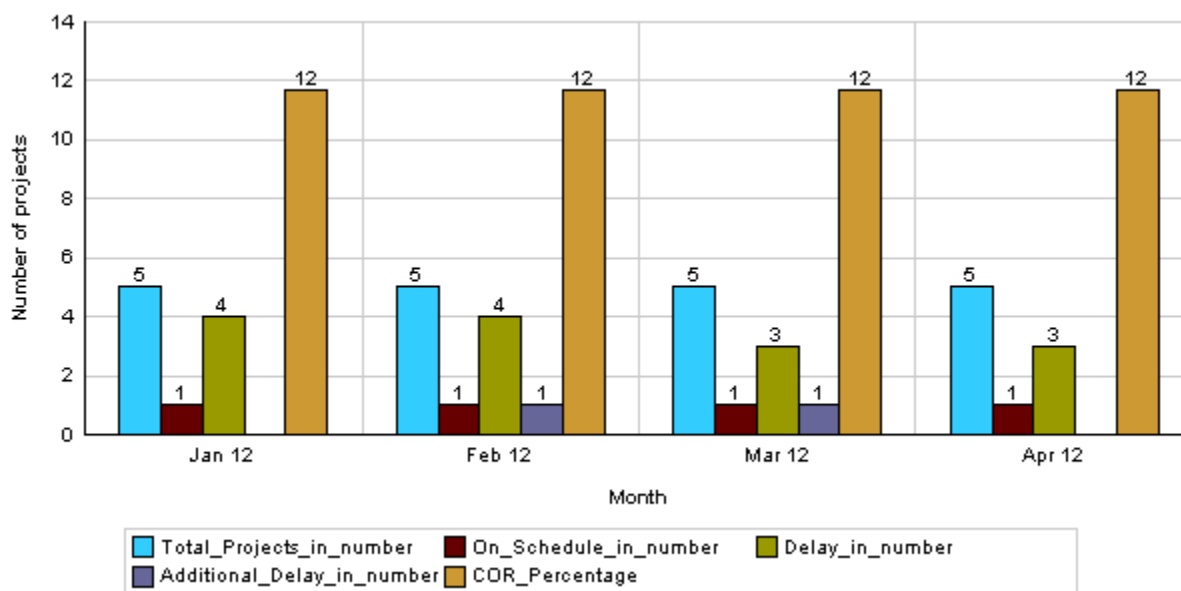


Civil Aviation Sector Sector Break-up of 3 Delayed projects in April 2012

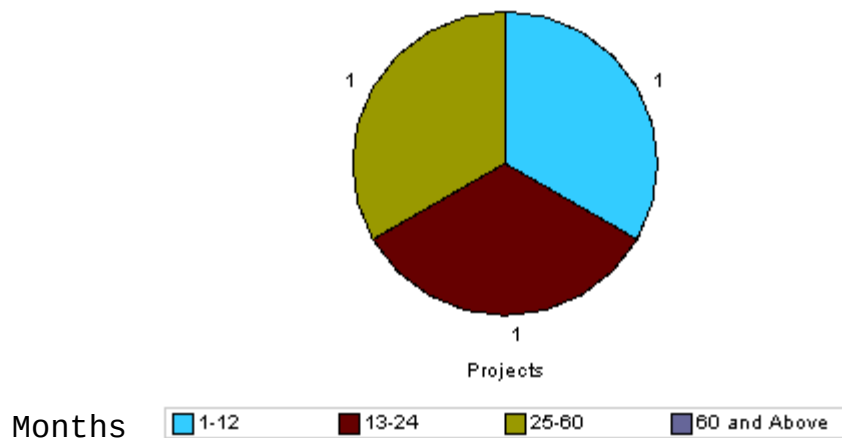


Trend and Graphical Analysis

Atomic Energy Sector

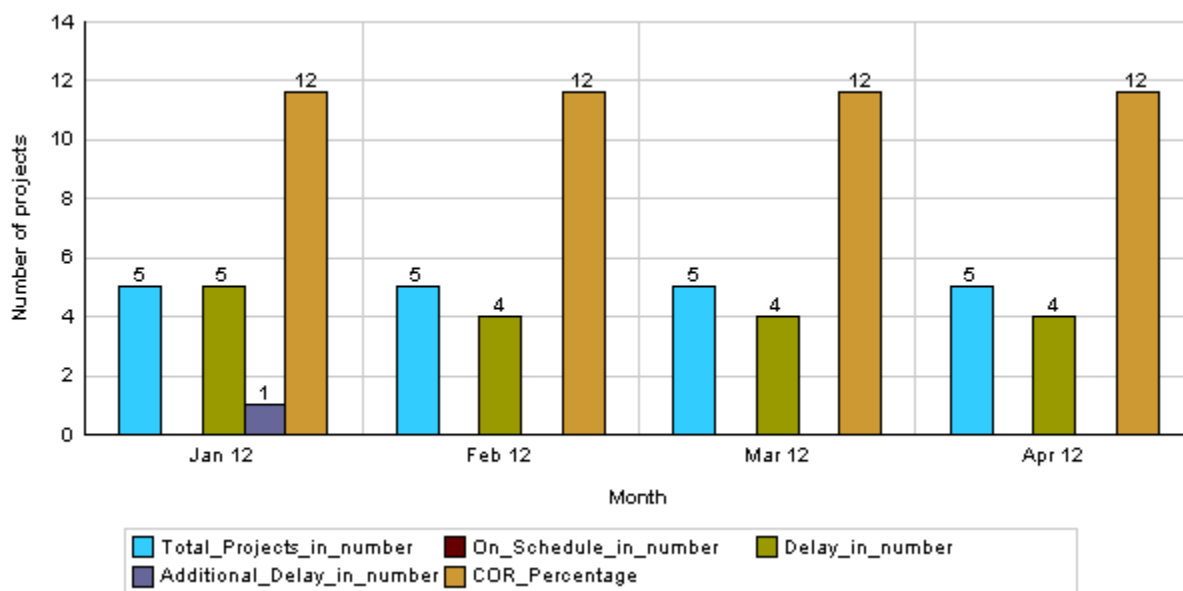

Atomic Energy Sector Sector Break-up of 4 Delayed projects in April 2012

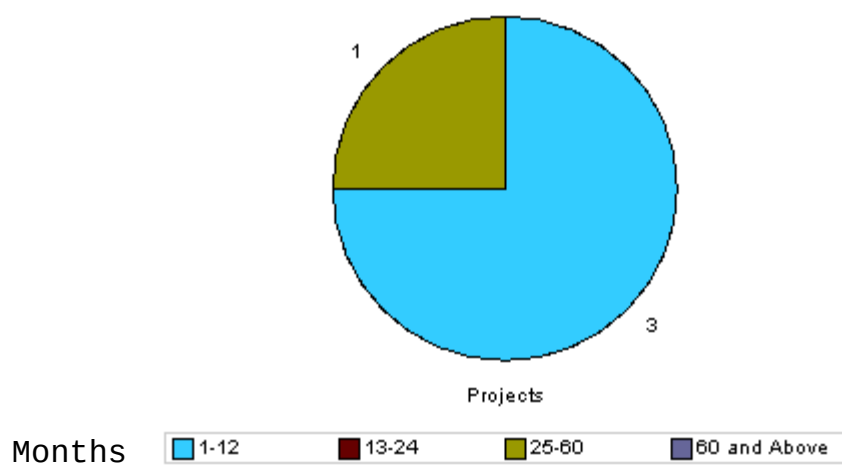

Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)			
		Original	Latest	Anticipated	Cumm Expenditure
Atomic Energy	5	41,548.29	41,548.29	46,386.29	22,118.84
Civil Aviation	5	5,021.58	5,228.58	5,611.07	4,219.76
Coal	51	33,815.11	35,022.73	37,312.15	12,005.65
Fertilisers	6	5,317.41	5,317.41	5,317.41	2,348.53
Steel	16	50,155.82	56,031.10	71,402.36	39,635.95
Petrochemicals	1	5,460.61	8,920.00	8,920.00	4,510.51
Petroleum	64	155,277.97	169,294.47	164,778.94	71,506.47
Power	102	211,144.68	215,027.96	225,276.41	107,653.57
Railways	131	65,286.30	95,083.90	141,884.10	58,372.89
Road Transport & Highways	148	92,330.10	92,496.60	94,297.43	58,943.43
Shipping & Ports	22	17,207.90	18,569.42	18,722.87	6,982.00
Telecommunications	15	6,161.00	6,164.88	6,101.79	1,769.14
Urban Development	4	44,245.18	44,304.08	49,518.08	2,504.31
Water Resources	1	542.90	542.90	1,187.00	35.49
Grand total	571	733,514.85	793,552.32	876,715.90	392,606.54

Sector Wise Details

(Apr,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
Atomic Energy									
1	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00	11,459.00	1,679.00	12/2015	11/2016	11(O)	0/70
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00	15,824.00	14,714.00	12/2008	03/2013	51(O)	39/106
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00	5,677.00	3,641.60	09/2010	01/2012	16(O)	6/80
4	RAJASTHAN ATOMIC POWER PROJECT - 7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00	12,320.00	1,000.00	12/2016	03/2017	3(O)	0/69
5	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29	1,106.29	1,084.24	04/2011	04/2012	12(O) 12(R)	0/0
Total			41,548.29	46,386.29	22,118.84				45/325
Civil Aviation									
6	C/O INTEGRATED PASSENGER TER. BULD. NSCB AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51	2,325.00	1,927.29	05/2011	10/2012	17(O) 7(R)	0/0
7	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46	309.46	182.97	01/2011	04/2013	27(O) 0(R)	0/0
8	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61	335.61	105.04	05/2012	08/2012	3(O)	0/0
9	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00	2,015.00	1,658.13	01/2011	02/2012	13(O) 0(R)	0/0
10	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00	626.00	346.33	06/2013	06/2013	0(O)	0/0
Total			5,021.58	5,611.07	4,219.76				0/0
Coal									
11	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	09/2006	212.34	779.26	281.16	03/2013	10/2014	19(O) 25(R)	7/22
12	AMLAI OC EXPANSION SECTOR 1.50 MTY - [N06000082]SECL,Chhatisgarh	11/2009	150.59	198.59	95.25	-	03/2016	-	0/6

Sector Wise Details

(Apr,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original /Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
13	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]NCL,Madhya pradesh	05/2006	1,352.04 1,143.54	1,143.54	317.40	03/2014 03/2016	03/2016	24(O) 0(R)	2/2
14	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Orissa	08/2008	207.28 -	207.28	99.57	03/2012 03/2012	03/2014	24(O) 24(R)	5/7
15	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhandd	04/2006	471.66 341.63	341.63	108.58	03/2011 03/2012	03/2013	24(O) 12(R)	0/2
16	BALRAM OCP EXTENSION,MCL (8.00 Mty) - [N06000044]MCL,Orissa	12/2007	172.08 -	172.08	101.78	03/2010 -	03/2015	60(O) -	4/4
17	BAROUD OC EXPANSION (RCE)-3MTY - [N06000099]SECL,Chhatisgarh	04/2012	258.56 -	258.56	33.55	03/2016 -	03/2016	0(O) -	0/0
18	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]MCL,Orissa	12/2007	490.00 -	490.10	108.89	03/2017 03/2017	03/2017	0(O) 0(R)	6/12
19	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019]NCL,Multi State	11/2006	168.97 168.97	168.97	40.35	03/2014 03/2014	03/2014	0(O) 0(R)	1/2
20	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04 535.10	535.10	161.77	03/2012 03/2015	03/2015	36(O) 0(R)	0/0
21	Batura OCP (2.0 MTY) - [N06000049]SECL,Madhya pradesh	09/2008	203.82 -	203.82	-	03/2015 -	03/2015	0(O) -	0/1
22	CHURCHA ROUG (1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35 -	462.35	272.54	- 03/2014	03/2014	- 0(R)	0/7
23	Churi Benti UG - [N06000083]CCL,Jharkhandd	06/2007	163.51 -	163.51	34.06	03/2011 03/2012	03/2014	36(O) 24(R)	1/2
24	DIPKA EXPANSION OCP (SECL) (20-25 MTY) - [060100094]SECL,Chhatisgarh	07/2005	1,268.53 -	1,943.66	1,271.50	03/2010 -	03/2014	48(O) -	0/12
25	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,Chhatisgarh	07/2005	1,667.55 -	2,675.67	1,391.03	03/2010 -	03/2014	48(O) -	0/15
26	GOPAL PRASAD OCP - [N06000042]MCL,Orissa	02/2008	395.87 -	395.87	59.64	03/2015 03/2015	03/2015	0(O) 0(R)	2/12
27	HINGULA OC-II EXP PH-III (15 MTY) - [N06000068]MCL,Orissa	11/2008	475.93 -	479.53	94.67	03/2013 03/2013	03/2013	0(O) 0(R)	5/7
28	JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh	09/2008	152.43 -	152.43	-	- -	03/2015	- -	0/6
29	JALAGAM VENGALA RAO OCP - [N06000094]SCCL,Andhra Pradesh	07/2011	447.06 -	447.06	-	03/2015 -	03/2015	0(O) -	4/31
30	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	03/2013	467.78 -	467.78	12.31	03/2013 -	03/2013	0(O) -	4/83
31	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18 -	287.17	-	03/2011 -	03/2015	48(O) -	0/1
32	KAKATIYA LAONGWALL - [N06000048]SCCL,Multi State	12/2008	453.63 -	453.63	71.37	12/2012 -	01/2015	25(O) -	8/44
33	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Orissa	12/2007	457.77 -	457.77	118.26	03/2013 03/2013	03/2013	0(O) 0(R)	6/11
34	KARMA OCP - [N06000088]CCL,Jharkhandd	06/2009	162.46 -	162.46	34.19	03/2014 -	03/2014	0(O) -	0/0
35	KARTALI (EAST) OCP(2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44 -	178.44	-	- -	03/2014	- -	0/6

Sector Wise Details

(Apr,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
36	KHADIA EXPANSION OPENCAST PROJECT 4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28 1,131.28	1,131.28	-	03/2018 03/2018	03/2018	0(O) 0(R)	0/0
37	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Uttar Pradesh	05/2006	789.88 741.62	741.62	331.78	03/2010 -	03/2013	36(O) -	2/2
38	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Orissa	01/2005	302.96 -	302.96	91.51	03/2010 -	03/2014	48(O) -	9/11
39	KUSMUNDA EXPN.OCP(SECL)(10-15MTY) - [N06000008]SECL,Chhatisgarh	06/2006	737.65 -	1,188.31	683.58	- 03/2013	03/2013	- 0(R)	0/8
40	Kistaram OCP - [N06000089]SCCL,Andhra Pradesh	11/2010	242.29 -	242.29	-	03/2015 -	03/2015	0(O) -	0/28
41	MAGADH OC (CCL) - [N06000015]CCL,Jharkhandd	07/2006	469.78 706.40	706.40	18.16	07/2012 03/2014	03/2016	44(O) 24(R)	1/2
42	MANIKPUR OC EXPANTION (3.50 MTY) - [N06000081]SECL,Chhatisgarh	11/2009	321.42 -	321.50	210.36	- 03/2014	03/2014	- 0(R)	0/5
43	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19 -	181.19	36.96	03/2012 -	03/2013	12(O) -	10/34
44	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhandd	08/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015	0(O) -	0/0
45	Muraidih UG - [N06000096]BCCL,Jharkhandd	02/2011	339.88 -	339.88	-	04/2014 -	04/2014	0(O) -	0/0
46	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu	06/2011	5,907.11 -	5,907.11	15.94	12/2015 -	12/2015	0(O) -	0/33
47	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40 -	259.40	1.20	03/2012 -	03/2015	36(O) -	0/1
48	North Urimari OCP - [N06000084]CCL,Jharkhandd	12/2007	179.87 -	179.87	62.60	03/2012 03/2012	03/2014	24(O) 24(R)	0/2
49	PELMA OCP(10.00MTY) - [N06000045]SECL,Chhatisgarh	07/2008	448.32 -	448.32	-	03/2015 -	03/2015	0(O) -	0/1
50	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77 -	339.77	0.82	03/2014 -	03/2015	12(O) -	0/1
51	Purnadih OCP - [N06000085]CCL,Jharkhandd	07/2008	210.98 -	210.98	34.18	03/2013 -	03/2013	0(O) -	0/2
52	RAJMAHAL OC EXP. - [N06000056]ECL,Multi State	02/2006	50.08 -	153.82	23.71	03/2011 -	03/2014	36(O) -	0/1
53	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97 -	418.97	86.44	03/2012 -	03/2013	12(O) -	24/27
54	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,Andhra Pradesh	07/2011	162.76 -	162.76	2.42	03/2015 -	03/2015	0(O) -	4/29
55	RKP OCP PHASE-I - [N06000079]SCCL,Andhra Pradesh	03/2010	209.78 -	209.78	21.83	03/2015 -	03/2015	0(O) -	4/31
56	Rajrappa RCE OCP - [N06000087]CCL,Jharkhandd	12/2009	510.85 -	510.85	284.57	03/2016 -	03/2016	0(O) -	1/2

Sector Wise Details

(Apr,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
57	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03 -	249.03	45.80	03/2012 -	03/2012	0(O) -	11/42
58	TALABIRA OCP - [N06000043]MCL,Orissa	03/2008	447.72 -	447.72	47.56	03/2016 03/2016	03/2016	0(O) 0(R)	1/12
59	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 3,027.59	3,027.59	2,400.12	06/2009 -	03/2013	45(O) -	19/24
60	TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 4,909.54	4,909.54	2,801.35	03/2012 -	03/2014	24(O) -	0/39
61	Tapin OCP - [N06000086]CCL,Jharkhand	08/2008	264.68 -	264.68	96.89	03/2012 03/2013	03/2014	24(O) 12(R)	0/2
Total			33,815.11 -	37,312.15	12,005.65				141/634
Fertilisers									
62	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGE OVER PROJ - [N08000005]NFL,Punjab	01/2010	1,294.19 -	1,294.19	551.85	01/2013 -	01/2013	0(O) -	0/5
63	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00 -	438.00	218.37	07/2011 -	07/2012	12(O) -	0/0
64	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00 -	325.00	174.37	07/2011 -	04/2012	9(O) -	0/0
65	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,Punjab	01/2010	1,478.63 -	1,478.63	553.49	01/2013 01/2013	01/2013	0(O) 0(R)	8/8
66	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGE OVER PROJE - [N08000004]NFL,Haryana	01/2010	1,292.84 -	1,292.84	544.15	01/2013 -	01/2013	0(O) -	0/5
67	THAL AMMONIA REVAMP PROJECT - [N08000003]RCF,Haryana	01/2009	488.75 -	488.75	306.30	04/2012 04/2012	04/2012	0(O) 0(R)	12/22
Total			5,317.41 -	5,317.41	2,348.53				20/40
Steel									
68	1.2 MTPA PELLET PLANT DONIMALAI - [N12000072]NMDC,Karnataka	04/2011	572.00 -	572.00	-	04/2013 -	04/2013	0(O) -	0/0
69	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00 -	350.00	241.50	08/2010 08/2010	06/2012	22(O) 22(R)	0/1
70	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00 -	343.58	246.84	02/2011 02/2011	07/2012	17(O) 17(R)	2/3
71	7.0 MTPA KUMARASWAMY IRON ORE MINE - [N12000073]NMDC,Karnataka	02/2011	898.55 -	898.55	-	05/2013 -	05/2013	0(O) -	0/0

Sector Wise Details

(Apr,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
72	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]SAIL,Chhatisgarh	07/2007	232.93	232.93	191.33	05/2011	05/2012	12(O)	1/1
73	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00	450.00	192.17	05/2012	02/2013	9(O) 9(R)	1/2
74	Bailadila Iron Ore Deposit- IIB(NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89	607.17	327.39	12/2011	10/2012	10(O) 7(R)	15/21
75	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	08/2007	108.00	216.68	77.68	10/2012	10/2012	0(O) 0(R)	3/4
76	ENHANCEMENT OF PROD. CAP. AT BOLANI I/O MINES - [N12000075]SAIL,Orissa	11/2011	254.55	254.55	5.54	-	11/2013	-	0/1
77	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	5,185.00	17,265.00	5,179.68	-	09/2013	-	18/27
78	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhandd	01/2008	3,316.00	6,325.00	2,624.65	-	10/2012	-	10/16
79	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,West Bengal	06/2009	2,875.00	2,875.00	750.85	12/2012	03/2013	3(O)	5/12
80	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00	16,408.00	13,087.79	-	12/2012	-	13/19
81	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00	12,291.00	9,513.66	10/2009	10/2012	36(O) 0(R)	59/64
82	EXPENSION OF ROURKELA STEEL PLANT - [N12000056]SAIL,Orissa	09/2008	11,812.00	11,812.00	6,841.66	11/2013	03/2013	-8(O)	5/14
83	Rebuilding of coke oven battery No.1 and 2 (Bokar - [N12000033]SAIL,Jharkhandd	10/2007	500.90	500.90	355.21	-	02/2012	-	3/3
Total			50,155.82	71,402.36	39,635.95				135/188
Petrochemicals									
84	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,Assam	04/2006	5,460.61	8,920.00	4,510.51	12/2013	12/2013	0(O) 0(R)	10/30
Total			5,460.61	8,920.00	4,510.51				10/30
Petroleum									
85	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00	820.00	-	06/2012	04/2013	10(O)	0/0
86	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64	2,163.64	926.83	06/2012	12/2012	6(O)	0/0
87	ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11	370.11	211.24	04/2011	07/2012	15(O)	0/0
88	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35	977.00	282.27	12/2011	01/2013	13(O)	0/0

Sector Wise Details

(Apr,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
89	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, Assam	03/2009	2,465.15 -	2,378.86	589.72	03/2013 -	03/2014	12(O) -	0/0
90	Ahmedabad Redevelopment - [N16000120]ONGC, Gujarat	11/2010	1,916.10 -	1,916.10	5.57	12/2014 -	12/2014	0(O) -	0/0
91	Ankleswar Redevelopment - [N16000122]ONGC, Gujarat	11/2010	2,189.63 -	2,189.63	4.84	12/2014 -	12/2014	0(O) -	0/0
92	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL, Multi State	12/2009	540.92 -	460.70	195.06	07/2012 07/2012	03/2013	8(O) 8(R)	0/16
93	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]IOCL, Haryana	11/2009	341.50 -	341.50	61.38	02/2013 -	02/2013	0(O) -	30/42
94	CDU/VDU-II - [N16000110]CPCL, Tamil Nadu	03/2010	333.99 -	333.99	120.71	- -	09/2012	- -	23/36
95	COMPRESSOR STATIONS (KAILARAS AND CHAINSA) - [N16000054]GAIL, Multi State	11/2007	1,167.00 -	798.00	707.41	04/2011 12/2011	09/2012	17(O) 9(R)	2/2
96	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC, Multi State	06/2007	736.65 -	736.65	287.21	09/2011 -	12/2012	15(O) -	0/0
97	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC, Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	5,314.79	05/2010 05/2012	07/2012	26(O) 2(R)	0/0
98	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL, Tamil Nadu	01/2008	224.00 299.00	299.00	320.40	02/2011 08/2011	08/2011	6(O) 0(R)	0/0
99	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER - [N16000127]ONGC, Assam	06/2010	202.94 -	202.94	-	01/2014 -	01/2014	0(O) -	0/0
100	CONSTRUCTION OF TANKS AND BLENDING FACILITY AT VAD - [N16000115]IOCL, Gujarat	02/2009	267.00 -	267.00	195.93	09/2012 09/2012	09/2012	0(O) 0(R)	0/0
101	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC, Maharashtra	03/2011	861.79 -	756.65	5.73	05/2013 -	05/2013	0(O) -	0/0
102	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC, Multi State	11/2010	331.20 -	269.10	-	08/2013 -	01/2014	5(O) -	0/0
103	Construction of 6 ETPs - [N16000117]ONGC, Gujarat	03/2009	302.26 -	302.26	19.83	09/2012 -	12/2012	3(O) -	0/0
104	Construction of one Multipurpose Support Vessel - [N16000103]ONGC, Multi State	01/2010	723.64 -	723.64	-	03/2013 -	11/2013	8(O) -	0/0
105	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL, Multi State	06/2009	4,543.43 4,508.38	2,300.00	1,706.48	03/2012 08/2012	08/2012	5(O) 0(R)	0/17
106	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip) - [N16000089]IOCL, Maharashtra	12/2009	1,584.00 -	1,584.00	13.25	- -	-	- -	0/0
107	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC, Multi State	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	12/2012	80(O) 6(R)	0/0

Sector Wise Details

(Apr,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
108	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	3,499.88	08/2010 03/2012	12/2013	40(O) 21(R)	0/0
109	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,273.53	09/2010 03/2012	04/2013	31(O) 13(R)	0/0
110	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	825.10	07/2010 05/2012	07/2012	24(O) 2(R)	0/0
111	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	04/2013	52(O) 0(R)	0/0
112	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON - [N16000009]BRPL,Assam	06/2006	1,431.91 1,646.39	1,690.13	1,596.80	09/2009 -	-	- -	0/0
113	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 2,174.00	2,174.00	861.04	09/2012 05/2012	05/2012	-4(O) 0(R)	0/76
114	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	1,156.52	09/2011 03/2012	09/2012	12(O) 6(R)	0/0
115	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	36.64	03/2013 -	04/2013	1(O) -	0/0
116	Development of C-26 Cluster Fields - [N16000133]ONGC,Maharashtra	03/2012	2,592.17 -	2,592.17	-	05/2014 -	03/2015	10(O) -	0/0
117	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 -	3,241.03	199.90	03/2013 -	04/2013	1(O) -	0/0
118	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	7.33	11/2012 -	05/2013	6(O) -	0/0
119	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	2,523.00	47.45	01/2014 -	01/2014	0(O) -	0/0
120	EURO-IV DHD - [N16000109]CPCL,Tamil Nadu	09/2008	2,615.69 -	2,615.69	1,894.77	- -	-	- -	114/116
121	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00 -	1,000.00	94.70	01/2013 -	01/2013	0(O) -	15/18
122	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MU - [N16000081]BPCL,Maharashtra	04/2008	825.00 1,827.00	1,827.00	481.23	04/2013 04/2013	04/2013	0(O) 0(R)	0/167
123	Heera and South Heera Redevelopment Ph-II - [N16000132]ONGC,Maharashtra	03/2012	5,608.40 -	5,608.40	-	05/2015 -	05/2015	0(O) -	0/0
124	INTEGRATED OFFSHORE CRUDE OIL HANDLING FACILITIES - [N16000090]IOCL,Orissa	12/2009	1,492.33 -	1,300.00	1,093.96	06/2012 06/2012	06/2012	0(O) 0(R)	6/8
125	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,481.56	03/2007 03/2017	03/2017	120(O) 0(R)	6/6
126	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	594.10	03/2007 03/2014	03/2014	84(O) 0(R)	3/3
127	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	265.66	03/2006 03/2013	03/2013	84(O) 0(R)	6/6

Sector Wise Details

(Apr,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
128	Integrated Development of B-127 fields - [N16000131]ONGC, Maharashtra	12/2011	2,059.63	2,059.63	-	03/2015	03/2015	0(O)	0/0
129	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL, Multi State	07/2009	7,596.18	7,596.18	2.20	01/2013	07/2015	30(O)	0/0
130	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL, Haryana	11/2007	281.07	281.07	3.41	10/2010	12/2014	50(O)	0/0
131	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- - [N16000070]GAIL, Multi State	07/2009	238.68 252.37	204.00	169.73	01/2012	07/2012	6(O)	3/8
132	KOCHI KOOTTANAD BANGLORE MANGLORE PIPELINE PH-II - [N16000129]GAIL, Multi State	06/2009	2,915.00	2,915.00	885.82	12/2012 12/2012	04/2013	4(O) 4(R)	0/21
133	KOCHI-KOOTANAD BANGALORE-MANGALORE PIPELINE PROJEC - [N16000071]GAIL, Multi State	06/2009	348.00	261.00	193.21	03/2012 08/2012	08/2012	5(O) 0(R)	2/4
134	MRPL Phase-III Expansion - [N16000114]Mangalore Refin, Karnataka	08/2008	12,412.00 12,160.26	12,160.26	8,582.11	01/2012	10/2012	9(O)	0/0
135	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC, Maharashtra	01/2009	7,133.39	6,855.93	3,427.22	09/2012	09/2013	12(O)	0/0
136	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC, Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	6,939.45	05/2010 03/2013	03/2013	34(O) 0(R)	0/0
137	Mehesana Redevelopment - [N16000121]ONGC, Gujarat	11/2010	3,823.00	3,823.00	5.67	04/2015	04/2015	0(O)	0/0
138	North Tapti Gas Field Development - [N16000096]ONGC, Multi State	07/2008	589.70 755.76	755.76	549.84	03/2011 05/2011	10/2012	19(O) 17(R)	0/0
139	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC, Maharashtra	01/2007	740.02	740.02	479.11	03/2010 03/2012	05/2013	38(O) 14(R)	0/0
140	PARADIP REFINERY PROJECT - [N16000058]IOCL, Orissa	02/2009	29,777.00	30,426.00	15,205.00	11/2012 06/2013	06/2013	7(O) 0(R)	57/100
141	PARADIP-RAIPUR-SAMBALPUR-RANCHI PIPELINE - [N16000088]IOCL, Multi State	08/2009	1,793.00	1,400.00	606.13	09/2012 09/2012	09/2012	0(O) 0(R)	0/11
142	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL, Multi State	08/2010	8,140.00	8,140.00	1,018.62	02/2014	02/2014	0(O)	0/0
143	Polypropylene unit - [N16000113]Mangalore Refin, Karnataka	05/2009	1,803.78	1,803.78	556.74	07/2012	07/2012	0(O)	0/0
144	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL, Andhra Pradesh	01/2009	756.00	898.00	840.50	09/2011	03/2012	6(O)	0/0
145	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC, Maharashtra	05/2008	333.40 837.54	656.51	554.93	05/2010 04/2012	05/2012	24(O) 1(R)	0/0

Sector Wise Details

(Apr,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
146	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	288.04	165.42	08/2012 -	12/2012	4(O) -	0/0
147	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32 -	330.47	202.86	03/2012 03/2012	06/2012	3(O) 3(R)	0/20
148	Wax Project - [N16000101]NRL,Assam	06/2010	576.60 -	576.60	34.77	12/2013 12/2013	12/2013	0(O) 0(R)	0/0
Total			155,277.97 -	164,778.94	71,506.47				267/677
Power									
149	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	5,161.60	08/2012 -	03/2013	7(O) -	0/0
150	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32 -	1,347.32	1,031.20	02/2012 -	10/2012	8(O) -	0/0
151	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	1,075.12	567.70	05/2012 -	12/2012	7(O) -	0/0
152	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36 -	1,736.36	929.20	06/2012 -	12/2012	6(O) -	0/0
153	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04 -	7,341.04	4,218.00	08/2013 -	06/2014	10(O) -	5/18
154	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97 -	8,693.00	6,961.00	12/2009 12/2014	03/2016	75(O) 15(R)	26/47
155	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	3,065.00	- -	11/2014	- -	4/28
156	CHAMERA,STAGE-III (NHPC) - [180100241]NHPC,Himachal Pr.	08/2005	1,405.63 -	2,084.00	1,815.30	08/2010 08/2011	06/2012	22(O) 10(R)	0/2
157	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J and K	08/2006	621.26 -	621.28	733.22	02/2011 -	10/2012	20(O) -	2/4
158	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNA - [N18000111]PGCIL,Andhra Pradesh	08/2011	1,637.34 -	1,637.34	173.70	08/2014 -	08/2014	0(O) -	0/0
159	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA - [N18000126]PGCIL,Andhra Pradesh	03/2012	206.44 -	206.44	21.90	06/2014 -	06/2014	0(O) -	0/0
160	Common System Associated with Coastal Energen Priv - [N18000103]PGCIL,Tamil Nadu	09/2011	1,940.13 -	1,940.13	197.90	09/2014 -	09/2014	0(O) -	0/0
161	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96 -	975.96	829.70	10/2009 -	12/2012	38(O) -	20/20

Sector Wise Details

(Apr,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
162	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80	1,272.80	291.40	11/2012	09/2013	10(O)	0/0
163	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123]PGCIL,Multi State	03/2012	198.63	198.63	-	09/2014	09/2014	0(O)	0/0
164	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA - [N18000101]PGCIL,Chhatisgarh	05/2011	1,961.87	1,961.87	268.50	05/2014	05/2014	0(O)	0/0
165	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52	1,719.52	431.90	08/2013	08/2013	0(O)	0/0
166	IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS - [N18000082]PGCIL,Bihar	02/2010	215.86	215.86	179.30	06/2012	06/2012	0(O)	0/0
167	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,Bihar	12/2011	901.77	901.77	52.80	08/2014	08/2014	0(O)	0/0
168	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH - [N18000110]PGCIL,Multi State	08/2011	1,391.97	1,391.97	182.10	12/2013	12/2013	0(O)	0/0
169	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000107]PGCIL,Chhatisgarh	08/2011	1,391.97	1,391.97	182.10	12/2013	12/2013	0(O)	0/0
170	INTERCONNECTION BETWEEN ELECTTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32	160.32	38.90	10/2012	03/2013	5(O)	0/0
171	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45	1,007.16	831.40	12/2007	12/2009	24(O)	0/18
172	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pr.	12/2004	2,496.90	2,496.90	1,829.23	05/2013	03/2017	46(O)	2/22
173	KISHANGANGA HEP - [N18000031]NHPC,J and K	07/2007	2,238.67	3,642.00	1,411.76	01/2016	11/2016	10(O)	0/2
174	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pr.	10/2002	4,527.15	4,527.15	4,260.00	04/2009	03/2014	59(O)	0/9
175	KUDANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29	1,779.29	1,828.98	09/2008	-	-	3/37
176	LINE BAYS AND REACTOR PROVISIONS AT POWERGRID SUBSTATIONS AS - [N18000124]PGCIL,Madhya pradesh	03/2012	213.78	213.78	-	03/2014	03/2014	0(O)	0/0
177	LOHARINAG-PAL HEP(4X150MW) - [N18000005]NTPC,Uttaranchal	06/2006	2,895.10	2,895.10	690.00	11/2011	12/2012	13(O)	6/34
178	MAUDA TRANSMISSION SYSTEM - [N18000084]PGCIL,Maharashtra	02/2010	469.38	469.38	223.20	10/2012	05/2012	-5(O)	0/0
179	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28	6,010.89	4,047.00	08/2012	03/2013	7(O)	10/16

Sector Wise Details

(Apr,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
180	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J and K	08/2006	611.01 -	936.00	729.82	08/2010 09/2011	01/2013	29(O) 16(R)	0/3
181	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	4,502.50	08/2013 -	09/2014	13(O) -	0/0
182	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69 -	317.69	180.40	11/2011 11/2011	06/2012	7(O) 7(R)	0/0
183	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	226.20	02/2012 -	06/2013	16(O) -	0/0
184	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	520.48	11/2011 -	06/2013	19(O) -	0/0
185	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	324.10	11/2011 -	06/2013	19(O) -	0/0
186	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68 -	182.68	42.50	01/2013 -	01/2013	0(O) -	0/0
187	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64 -	752.64	161.30	07/2013 -	07/2013	0(O) -	0/0
188	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	386.00	04/2013 -	06/2013	2(O) -	0/0
189	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII - [N18000091]PGCIL,Multi State	12/2010	209.78 -	209.78	52.20	08/2013 -	08/2013	0(O) -	0/0
190	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,Multi State	11/2011	723.63 -	723.63	40.40	11/2014 -	11/2014	0(O) -	0/0
191	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	383.60	11/2012 -	06/2013	7(O) -	0/0
192	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.56 -	2,716.00	1,788.59	10/2010 12/2011	01/2013	27(O) 13(R)	0/1
193	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pr.	09/2002	3,919.59 -	5,524.00	3,405.19	09/2009 07/2014	07/2014	58(O) 0(R)	1/20
194	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pr.	12/2008	573.99 -	573.99	314.41	08/2012 08/2013	09/2014	25(O) 13(R)	9/19
195	RAMPUR HEP(412 MW) - [N18000024]SJVN,L,Himachal Pr.	01/2007	2,047.03 -	2,047.03	1,658.86	01/2012 -	09/2013	20(O) -	0/0
196	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	3,163.00	10/2012 -	03/2013	5(O) -	9/16
197	SIPAT STPP STAGE - I (NTPC) - [180100229]NTPC,Chhatisgarh	12/2003	8,323.39 -	8,323.39	8,194.00	12/2009 12/2011	05/2012	29(O) 5(R)	59/60

Sector Wise Details

(Apr,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
198	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pr.	09/2003	6,285.33	10,667.00	5,653.06	09/2010 08/2014	12/2015	63(O) 16(R)	11/11
199	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36	170.36	36.10	04/2013	04/2013	0(O)	0/0
200	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95	2,360.95	1,916.40	08/2012	12/2012	4(O)	0/0
201	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10	196.10	132.50	07/2011	06/2012	11(O)	0/0
202	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR - [N18000116]PGCIL,Chhatisgarh	12/2011	1,746.65	1,746.65	47.90	08/2014	08/2014	0(O)	0/0
203	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP P - [N18000120]PGCIL,Maharashtra	02/2012	1,310.85	1,310.85	93.00	02/2015	02/2015	0(O)	0/0
204	SYSTEM STRENGTHENING IN RAIPUR- WARDHA CORRIDOR FOR IPP PROJEC - [N18000117]PGCIL,Chhatisgarh	01/2012	1,422.85	1,422.85	95.10	01/2015	01/2015	0(O)	0/0
205	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,Multi State	12/2011	297.33	297.33	21.80	08/2014	08/2014	0(O)	0/0
206	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,Multi State	10/2011	487.49	487.49	51.50	06/2014	06/2014	0(O)	0/0
207	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61	276.61	134.40	04/2012	04/2012	0(O)	0/0
208	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34	232.34	94.98	06/2012	06/2012	0(O)	0/0
209	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83	1,216.83	704.20	08/2012	12/2012	4(O)	0/0
210	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttaranchal	11/2006	2,978.48	2,978.48	1,457.00	03/2013	09/2015	30(O)	2/13
211	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38	1,501.75	1,112.46	09/2009	06/2013	45(O)	0/0
212	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92	1,628.39	1,476.77	03/2007	09/2012	66(O)	25/25
213	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00 2,978.86	2,978.86	321.09	07/2010 02/2016	02/2016	67(O) 0(R)	1/10
214	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000108]PGCIL,Madhya pradesh	07/2011	181.93	181.93	45.30	07/2013	07/2013	0(O)	0/0

Sector Wise Details

(Apr,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
215	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000118]PGCIL,Gujarat	01/2012	259.28 -	259.28	7.30	01/2014 -	01/2014	0(O) -	0/0
216	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND W - [N18000113]PGCIL,Multi State	12/2011	2,422.66 -	2,422.66	72.40	08/2014 -	08/2014	0(O) -	0/0
217	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART- - [N18000129]PGCIL,Multi State	02/2012	3,201.44 -	3,201.44	-	10/2014 -	10/2014	0(O) -	0/0
218	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37 -	297.91	326.43	07/2011 -	09/2012	14(O) -	0/0
219	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	4,824.12	2,687.70	10/2012 -	09/2013	11(O) -	0/0
220	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR - [N18000077]PGCIL,West Bengal	04/2010	4,404.57 -	4,404.57	254.50	01/2015 -	01/2015	0(O) -	0/0
221	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL,Multi State	03/2011	2,569.25 -	2,569.25	428.90	03/2014 -	03/2014	0(O) -	0/0
222	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) - [180100260]PGCIL,Bihar	12/2005	3,779.46 -	3,779.46	3,681.30	09/2009 -	06/2012	33(O) -	11/30
223	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM - [N18000090]PGCIL,Andhra Pradesh	12/2010	779.21 -	779.21	358.20	08/2013 -	08/2013	0(O) -	0/0
224	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000121]PGCIL,Andhra Pradesh	02/2012	324.33 -	324.33	1.20	08/2014 -	08/2014	0(O) -	0/0
225	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000122]PGCIL,Andhra Pradesh	02/2012	1,927.16 -	1,927.16	17.20	10/2014 -	10/2014	0(O) -	0/0
226	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24 -	557.24	549.00	01/2010 -	02/2013	37(O) -	0/22
227	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	149.00	11/2011 -	03/2013	16(O) -	0/0
228	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88 -	7,031.88	3,576.30	12/2012 -	12/2012	0(O) -	0/0
229	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT - [N18000114]PGCIL,Gujarat	12/2011	552.44 -	552.44	38.40	02/2014 -	02/2014	0(O) -	0/0

Sector Wise Details

(Apr,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
230	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL, Madhya Pradesh	08/2011	425.51 -	425.51	49.50	10/2013 -	10/2013	0(O) -	0/0
231	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL, Maharashtra	07/2011	181.93 -	181.93	-	07/2013 -	07/2013	0(O) -	0/0
232	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CH - [N18000105]PGCIL, Multi State	09/2011	1,366.34 -	1,366.34	133.10	12/2013 -	12/2013	0(O) -	0/0
233	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARK - [N18000104]PGCIL, Jharkhand	10/2011	558.26 -	558.26	62.80	11/2013 -	11/2013	0(O) -	0/0
234	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL, Orissa	09/2010	2,074.86 -	2,074.86	517.90	03/2013 -	03/2013	0(O) -	0/0
235	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL, Orissa	12/2010	2,743.19 -	2,743.19	536.20	12/2013 -	12/2013	0(O) -	0/0
236	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL, Multi State	03/2010	4,672.99 -	4,672.99	1,182.10	11/2012 -	03/2013	4(O) -	0/0
237	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR - [N18000112]PGCIL, Chhatisgarh	11/2011	2,127.51 -	2,127.51	183.10	07/2014 -	07/2014	0(O) -	0/0
238	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO, Tripura	07/2009	421.01 623.44	623.44	185.78	- 07/2013	07/2013	- 0(R)	0/29
239	TUIRIAL HE PROJECT (NEEPCO) - [180100165]NEEPCO, Mizoram	07/1998	368.72 913.63	913.63	307.53	07/2006 01/2014	02/2015	103(O) 13(R)	7/24
240	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO, Mizoram	01/2011	913.63 -	913.63	307.53	01/2014 -	01/2014	0(O) -	0/0
241	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL, Multi State	02/2010	2,144.00 -	2,144.00	731.60	12/2012 -	03/2013	3(O) -	0/0
242	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL, Multi State	03/2011	1,585.12 -	1,585.12	273.40	11/2013 -	11/2013	0(O) -	0/0
243	Transmission system for transfer of power from Gen. - [N18000098]PGCIL, Multi State	05/2010	250.03 -	250.03	50.50	01/2013 -	01/2013	0(O) -	0/0
244	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC, J and K	08/2005	1,729.29 -	1,794.00	1,715.58	11/2009 11/2011	02/2013	39(O) 15(R)	0/4
245	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC, Madhya Pradesh	01/2009	5,915.00 -	5,915.00	3,402.00	10/2012 -	03/2013	5(O) -	8/15

Sector Wise Details

(Apr,2012)

						Date of Commissioning		Delay w.r.t. Original /Revised (in months)	Milestones Achieved/ Total
S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
246	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttaranchal	08/2008	2,491.58 2,491.58	3,422.44	302.52	07/2014 -	05/2016	22(O) -	1/3
247	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23 -	5,221.23	3,123.60	07/2010 -	12/2012	29(O) -	20/20
248	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	477.69	398.00	09/2010 -	-	- -	0/0
249	WESTERN REGION SYSTEM STRENGHTENING SCHEME-XI - [N18000051]PGCIL,Multi State	02/2009	409.50 -	409.50	103.30	02/2012 02/2012	06/2012	4(O) 4(R)	0/0
250	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,Chhatisgarh	03/2012	9,569.76 -	9,569.76	18.60	06/2015 -	06/2015	0(O) -	0/0
Total			211,144.68 -	225,276.41	107,653.57				242/582
Railways									
251	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 -	1,141.75	355.97	03/2014 -	03/2014	0(O) -	0/0
252	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	227.42	250.82	12/2009 03/2011	03/2011	15(O) 0(R)	0/0
253	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 514.68	2,200.00	150.56	- -	06/2012	- -	0/0
254	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL,Uttar Pradesh	04/2003	230.73 399.73	399.50	322.76	03/2009 12/2008	12/2010	21(O) 24(R)	0/0
255	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 -	435.87	392.90	03/2011 03/2011	03/2011	0(O) 0(R)	0/0
256	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	548.95	516.67	06/1999 03/2011	03/2011	141(O) 0(R)	0/0
257	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	1,214.00	96.96	- -	-	- -	0/0
258	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.13 -	394.14	0.49	03/2013 -	03/2013	0(O) -	0/0
259	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 -	901.62	0.29	- -	-	- -	0/0
260	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,028.05	1,412.74	425.46	03/2005 12/2008	12/2015	129(O) 84(R)	0/0
261	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15 1,106.62	1,106.62	198.70	12/2010 03/2011	03/2011	3(O) 0(R)	0/0
262	BELAPUR-SEAWOOD-URAN ELECTRIF-IED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	1,512.86	184.74	03/2004 12/2010	12/2010	81(O) 0(R)	0/0

Sector Wise Details

(Apr,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
263	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34	2,393.49	17.74	04/2014	03/2014	-1(O)	0/0
264	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN - [N22000081]RVNL,Gujarat	09/2005	200.80	200.80	269.02	-	-	-	0/0
265	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20	687.20	-	03/2010	12/2012	33(O)	0/0
266	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52	350.00	-	-	03/2011	-	0/0
267	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00	3,230.01	2,387.21	04/2008	12/2015	92(O)	0/0
268	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52	207.52	126.13	12/2012	05/2013	5(O)	0/0
269	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36	196.95	177.90	03/2011	03/2011	0(O)	0/0
270	Bhuj-Naliya(GC) with extension from naliyate vayar - [N22000123]WR,Gujarat	04/2008	318.24	468.62	0.99	03/2012	03/2012	0(O)	0/0
271	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00	579.37	600.41	-	02/2012	-	0/0
272	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44	1,103.47	989.08	12/2012	12/2012	0(O)	0/0
273	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09	1,417.97	1,011.09	-	03/2012	-	0/0
274	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79	585.93	194.91	-	12/2013	-	0/0
275	CHURCHGATE-VIRAR:CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	653.84	1,302.12	608.97	06/2013	06/2012	-12(O)	0/0
276	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00	415.73	240.26	-	03/2012	-	0/0
277	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00	968.60	-	12/2012	-	-	0/0
278	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84	410.08	182.36	-	03/2013	-	0/0
279	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00	607.09	376.26	12/2012	12/2012	0(O)	0/0
280	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17	900.00	505.61	-	-	-	0/0
281	Dakshin-barasal-lakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51	533.38	80.26	12/2011	02/2012	2(O)	0/0
282	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10	171.10	141.55	03/2012	03/2012	0(O)	0/0

Sector Wise Details

(Apr,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original /Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
283	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	250.00	227.48	03/2011 -	03/2012	12(O) -	0/0
284	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	495.74	152.04	06/2013 06/2013	06/2013	0(O) 0(R)	0/0
285	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	634.13	550.42	03/1995 -	03/2013	216(O) -	0/0
286	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	270.00	258.21	02/2011 02/2011	03/2012	13(O) 13(R)	0/0
287	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 261.70	261.70	39.12	02/2006 -	12/2012	82(O) -	0/0
288	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 -	863.23	509.13	- -	-	- -	0/0
289	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	1,038.00	590.26	03/1998 -	03/1998	0(O) -	0/0
290	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	1,164.00	309.75	- 05/2009	05/2009	- 0(R)	0/0
291	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	611.03	89.65	12/2011 11/2013	11/2013	23(O) 0(R)	0/0
292	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	324.66	177.81	- -	03/2015	- -	0/0
293	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 1,185.00	1,185.00	210.20	- 09/2009	12/2011	- 27(R)	0/0
294	HARNOUT -SET. UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	337.30	222.07	- -	03/2012	- -	0/0
295	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	944.55	483.14	- -	-	- -	0/0
296	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 -	230.03	137.83	- -	-	- -	0/0
297	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	499.16	160.99	03/2007 03/2007	03/2014	84(O) 84(R)	0/0
298	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00 -	997.58	69.17	- -	-	- -	0/0
299	Himmatnagar - Udaipur Gauge Conversion (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 -	829.74	3.47	03/2015 -	03/2015	0(O) -	0/0
300	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30	847.76	854.37	06/2007 -	06/2007	0(O) -	0/0
301	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	1,043.56	630.07	03/2012 03/2012	03/2012	0(O) 0(R)	0/0
302	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	500.00	559.46	03/2012 03/2012	12/2012	9(O) 9(R)	0/0

Sector Wise Details

(Apr,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
303	JIRIBAM TO IMPHAL (TUPUJ)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 -	3,056.85	738.60	03/2011 03/2014	03/2016	60(O) 24(R)	0/0
304	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 -	653.46	101.57	03/2014 -	03/2014	0(O) -	0/0
305	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	262.82	212.77	03/2012 03/2012	03/2012	0(O) 0(R)	0/0
306	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	1,577.46	1,255.66	- -	02/2012	- -	0/0
307	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 -	750.89	474.97	- -	-	- -	1/1
308	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 229.88	712.00	713.06	- -	-	- -	0/0
309	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,041.79	728.94	12/2010 12/2010	03/2015	51(O) 51(R)	0/0
310	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	162.87	88.63	- -	-	- -	0/0
311	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	225.00	-	03/2009 03/2009	04/2013	49(O) 49(R)	0/0
312	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	1,100.00	206.43	- -	03/2012	- -	0/0
313	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 -	359.86	1.22	- -	03/2015	- -	0/0
314	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd	04/1996	371.36 -	452.35	402.20	- -	-	- -	0/0
315	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 1,099.20	1,099.20	1,223.54	07/2005 -	07/2005	0(O) -	0/0
316	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91 418.17	418.17	116.41	- -	-	- -	0/0
317	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 -	341.41	263.32	03/2012 03/2012	12/2012	9(O) 9(R)	0/0
318	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,045.00	1,047.00	9.41	- -	-	- -	0/0
319	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	302.23	331.25	- -	03/2011	- -	0/0
320	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 -	223.01	104.88	12/2012 -	03/2014	15(O) -	0/0
321	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	925.00	504.78	05/2008 03/2011	03/2011	34(O) 0(R)	0/0
322	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100007]NCR,Multi State	04/1985	158.77 432.46	540.96	558.07	03/1994 -	12/2011	213(O) -	0/0

Sector Wise Details

(Apr,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
323	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.98	227.94	200.21	03/2002 -	03/2012	120(O) -	0/0
324	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 -	4,255.37	3,055.16	03/2009 -	12/2013	57(O) -	0/0
325	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	480.00	0.35	07/2008 -	07/2008	0(O) -	0/0
326	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 -	218.19	153.90	- -	-	- -	0/0
327	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhandd	04/1995	184.00 900.05	900.05	519.54	12/2011 12/2011	03/2012	3(O) 3(R)	0/0
328	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	791.60	0.78	- -	-	- -	0/0
329	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	477.88	378.14	03/2012 03/2012	03/2012	0(O) 0(R)	0/0
330	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 -	900.00	239.07	- -	-	- -	0/0
331	MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N22000093]MRTP,Maharashtra	04/2003	3,125.20 4,174.40	4,501.80	4,334.00	06/2011 06/2011	06/2011	0(O) 0(R)	0/0
332	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	5,300.00	698.48	03/2014 03/2015	03/2015	12(O) 0(R)	0/0
333	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	645.00	119.71	- -	03/2012	- -	0/0
334	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]ECR,Bihar	04/1997	100.00 483.62	484.03	455.07	03/2012 03/2012	06/2012	3(O) 3(R)	0/0
335	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	883.00	583.44	02/2009 -	03/2012	37(O) -	0/0
336	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	730.00	367.19	07/2012 07/2012	07/2012	0(O) 0(R)	0/0
337	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 -	529.88	38.95	- -	-	- -	0/0
338	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 -	384.04	97.57	- -	03/2014	- -	0/0
339	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 -	1,655.80	1,086.71	12/2008 -	03/2014	63(O) -	0/0
340	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	703.17	240.74	- -	03/2015	- -	0/0
341	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 -	850.00	8.45	03/2015 -	03/2015	0(O) -	0/0

Sector Wise Details

(Apr,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
342	New Work for Construction of Metro railway - [N22000111]RVNL, West Bengal	04/2010	2,619.02 -	2,619.02	101.35	03/2016 -	03/2016	0(O) -	0/0
343	New Work for Construction of Metro railway from Ba - [N22000109]RVNL, West Bengal	04/2010	2,069.60 -	2,069.60	24.59	03/2014 03/2016	03/2016	24(O) 0(R)	0/0
344	New Work for Construction of Metro railway from NS - [N22000110]RVNL, West Bengal	04/2010	3,951.98 -	3,951.98	16.66	03/2016 -	03/2016	0(O) -	0/0
345	New Work for Construction of Metro railway from No - [N22000108]RVNL, West Bengal	04/2010	2,397.72 -	2,397.72	21.85	03/2016 -	06/2016	3(O) -	0/0
346	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, Andhra Pradesh	07/2006	743.00 -	1,117.11	-	03/2008 06/2008	06/2008	3(O) 0(R)	0/0
347	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL, Multi State	04/2005	240.00 -	355.00	-	03/2009 12/2009	03/2011	24(O) 15(R)	0/0
348	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL, West Bengal	09/2007	252.50 529.23	529.23	227.13	02/2010 -	12/2015	70(O) -	0/0
349	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR, Bihar	04/2001	624.47 1,389.98	1,389.98	1,230.99	10/2007 12/2012	12/2012	62(O) 0(R)	0/0
350	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, Andhra Pradesh	12/1994	124.43 495.68	925.30	557.79	- -	03/2012	- -	0/0
351	Pandabeswar-Chinipai doubling (ER) - [N22000118]ER, West Bengal	04/2004	225.68 293.74	293.74	135.90	12/2010 12/2010	12/2010	0(O) 0(R)	0/0
352	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR, Multi State	03/1998	280.00 842.35	1,029.00	733.51	- -	03/2013	- -	0/0
353	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL, Andhra Pradesh	04/2003	136.62 -	221.90	-	12/2007 03/2010	12/2010	36(O) 9(R)	0/0
354	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR, Bihar	04/2002	921.00 -	1,115.63	693.29	03/2009 12/2012	12/2012	45(O) 0(R)	0/0
355	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL, Orissa	04/1999	166.16 -	243.40	-	02/2009 02/2009	04/2013	50(O) 50(R)	0/0
356	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR, Gujarat	04/2006	196.97 -	196.97	213.97	03/2011 -	06/2012	15(O) -	0/0
357	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314]WCR, Madhya Pradesh	04/2001	727.13 727.13	1,225.00	223.90	- -	-	- -	0/0
358	RANCHI-LOHARDAGA(GC),SER - [220100214]SER, Jharkhand	04/1997	194.07 -	456.45	281.69	06/2004 -	12/2012	102(O) -	0/0
359	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR, Multi State	01/2004	915.70 -	1,717.29	1,174.67	- -	03/2013	- -	0/0
360	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL, Andhra Pradesh	06/2000	168.34 -	370.00	-	04/2003 03/2010	03/2010	83(O) 0(R)	0/0
361	REWARI-ROHTAK (NL),NR - [220100279](NR), Haryana	01/2004	149.38 330.23	476.68	519.90	02/2010 02/2011	02/2011	12(O) 0(R)	0/0

Sector Wise Details

(Apr,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
362	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER, Orissa	02/1996	57.94 604.04	639.97	177.14	03/1998 08/2005	08/2005	89(O) 0(R)	0/0
363	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	482.70	254.35	03/2013 -	03/2013	0(O) -	0/0
364	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 -	603.04	59.64	03/2012 -	03/2013	12(O) -	0/0
365	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	385.54	219.66	03/2010 -	03/2012	24(O) -	0/0
366	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	3,380.58	52.63	12/2015 -	12/2015	0(O) -	0/0
367	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/2001	143.92 258.60	279.59	232.09	03/2011 03/2011	03/2011	0(O) 0(R)	0/0
368	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23 -	818.29	-	02/2015 -	-	- -	0/0
369	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 -	516.23	180.47	03/2014 -	03/2014	0(O) -	0/0
370	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	810.78	109.94	- -	03/2013	- -	0/0
371	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	1,086.41	404.60	06/2005 07/2011	06/2016	132(O) 59(R)	0/0
372	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	1,188.91	485.56	- 12/2009	02/2012	- 26(R)	0/0
373	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 582.83	582.83	112.89	- -	-	- -	0/0
374	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 -	227.40	34.89	- -	-	- -	0/0
375	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 -	548.96	495.87	- -	-	- -	0/0
376	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 3,176.10	3,176.10	3,183.24	12/2006 08/2010	08/2010	44(O) 0(R)	0/0
377	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand	04/2008	167.73 -	167.73	41.63	03/2012 -	03/2012	0(O) -	0/0
378	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J and K	03/1995	2,500.00 8,000.00	20,000.00	7,933.78	03/2001 -	12/2017	201(O) -	0/0
379	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00 -	819.40	142.97	03/2010 06/2014	06/2014	51(O) 0(R)	0/0
380	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	1,389.62	279.96	03/2014 -	03/2014	0(O) -	0/0
381	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	356.87	160.51	- 03/2010	-	- -	0/0

Sector Wise Details

(Apr,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	Total		65,286.30	141,884.10	58,372.89				1/1
	<u>Road Transport & Highways</u>								
382	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, Bihar	05/2011	351.54	351.54	163.93	05/2013	03/2014	10(O)	0/0
383	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI, Bihar	05/2011	511.54	511.54	65.78	11/2013	11/2013	0(O)	0/0
384	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI, Meghalaya	02/2011	226.00	226.00	185.45	02/2014	02/2014	0(O)	0/0
385	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, Bihar	05/2011	664.00	664.00	15.15	02/2014	04/2014	2(O)	0/0
386	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, Bihar	10/2011	375.09	375.09	20.75	04/2014	04/2014	0(O)	0/0
387	2laning with PS Gopalganj-Chappra - [N24000190]NHAI, Bihar	12/2011	325.00	325.00	110.87	05/2014	05/2014	0(O)	0/0
388	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI, Multi State	02/2011	2,498.76	2,498.76	71.58	08/2014	08/2014	0(O)	0/0
389	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI, Gujarat	12/2010	1,008.50	1,008.50	1,079.10	06/2013	06/2013	0(O)	0/0
390	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI, Karnataka	03/2011	359.00	359.00	32.41	09/2013	07/2014	10(O)	0/0
391	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI, Gujarat	03/2011	785.50	785.50	438.69	08/2013	08/2013	0(O)	0/0
392	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, Bihar	01/2011	575.00	575.00	293.64	07/2013	07/2013	0(O)	0/0
393	4-laning of Barhi-Hazaribagh - [N24000191]NHAI, Jharkhand	02/2012	398.00	398.00	-	02/2014	02/2014	0(O)	0/0
394	4-laning of Brahmapore-Faraka - [N24000203]NHAI, Multi State	02/2011	998.79	998.79	498.45	08/2013	08/2013	0(O)	0/0
395	4-laning of Faraka-Raiganj - [N24000202]NHAI, Multi State	02/2011	1,078.84	1,078.84	527.55	08/2013	08/2013	0(O)	0/0
396	4-laning of Raiganj-Dalkola - [N24000204]NHAI, Multi State	02/2011	580.43	580.43	218.49	08/2013	08/2013	0(O)	0/0
397	AGRA-BYPASS(NS-1/UP-1), KM 176.8-13.03 NH-2,3 - [N24000098]NHAI, Uttar Pradesh	12/2003	348.16	465.50	151.69	09/2007	06/2013	69(O)	0/0
398	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI, Uttar Pradesh	04/2000	367.49	367.49	453.68	03/2005	06/2012	87(O)	0/0
399	AMRITSAR-PATHANKOT - [N24000147]NHAI, Punjab	05/2010	705.00	705.00	935.59	11/2012	06/2013	7(O)	0/0
400	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI, West Bengal	12/2003	221.82	221.82	278.86	11/2008	06/2012	43(O)	0/0
401	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI, Chhatisgarh	03/2005	190.00	190.00	254.19	01/2009	06/2012	41(O)	0/0

Sector Wise Details

(Apr,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original /Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
402	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56	390.56	631.65	02/2012	06/2012	4(O)	0/0
403	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70	228.70	182.07	02/2004	07/2012	101(O)	0/0
404	BAREILY-SITAPUR - [N24000200]NHAI,Uttar Pradesh	03/2011	1,046.00	1,046.00	75.09	09/2013	09/2013	0(O)	0/0
405	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,Rajasthan	12/2011	2,388.00	2,388.00	148.79	06/2014	06/2014	0(O)	0/0
406	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka	12/2010	480.00	480.00	331.15	-	10/2013	-	0/1
407	BHOPAL-SANCHI - [N24000192]NHAI,Madhya pradesh	10/2011	209.00	209.00	3.77	01/2013	01/2013	0(O)	0/0
408	BHUBANESWAR TO PURI - [N24000195]NHAI,Orissa	03/2011	500.29	500.29	329.15	08/2013	08/2013	0(O)	0/0
409	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80	237.80	238.58	06/2008	12/2012	54(O)	0/0
410	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00	195.00	196.85	06/2008	06/2012	48(O)	0/0
411	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00	230.00	224.58	06/2005	09/2012	87(O)	0/0
412	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61	217.61	188.81	04/2010	12/2012	32(O)	0/0
413	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00	281.31	179.23	02/2010	12/2013	46(O)	0/0
414	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00	852.00	540.98	03/2013	03/2013	0(O)	0/0
415	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,Karnataka	03/2011	839.00	839.00	56.04	-	12/2013	-	0/1
416	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00	1,585.00	881.80	05/2013	05/2013	0(O)	0/0
417	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37	353.37	231.86	10/2011	03/2014	29(O)	0/0
418	Chikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30	572.30	647.98	10/2011	06/2013	20(O)	0/0
419	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00	225.00	267.44	06/2008	06/2012	48(O)	0/0
420	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00	300.00	170.23	10/2008	12/2012	50(O)	0/0
421	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00	486.00	577.73	05/2010	12/2012	31(O)	0/0

Sector Wise Details

(Apr,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
422	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	953.00	593.00	306.72	07/2013	07/2013	0(O)	0/0
423	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu	06/2011	600.00	600.00	75.85	06/2013	06/2013	0(O)	0/0
424	DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka	12/2010	453.00	453.00	239.98	-	06/2013	-	1/1
425	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00	200.00	209.81	06/2008	06/2012	48(O)	0/0
426	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00	160.00	164.32	05/2008	06/2012	49(O)	0/0
427	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45	232.45	251.79	09/2010	12/2012	27(O)	0/0
428	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00	485.00	40.61	08/2013	08/2013	0(O)	0/0
429	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI,Chhatisgarh	01/2008	464.00	464.00	534.79	01/2011	06/2012	17(O)	0/0
430	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94	332.94	357.43	09/2008	12/2012	51(O)	0/0
431	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52	1,170.52	4.41	06/2011	10/2012	16(O)	0/0
432	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00	201.66	112.02	09/2008	06/2012	45(O)	0/0
433	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27	263.27	265.81	02/2004	06/2012	100(O)	0/0
434	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI,Uttar Pradesh	12/2003	275.00	275.00	304.24	09/2007	06/2012	57(O)	0/0
435	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00	1,141.00	177.37	08/2013	08/2013	0(O)	0/0
436	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16	198.16	202.60	04/2008	12/2012	56(O)	0/0
437	GUWAHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96	175.96	140.59	04/2008	12/2012	56(O)	0/0
438	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93	300.93	302.72	10/2009	12/2012	38(O)	0/0
439	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00	604.00	494.29	12/2009	12/2012	36(O)	0/0
440	Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10	1,509.10	1,299.10	09/2012	09/2012	0(O)	0/0
441	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70	1,673.70	2,406.10	10/2011	06/2012	8(O)	0/0

Sector Wise Details

(Apr,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
442	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI, West Bengal	04/2000	273.00 -	522.00	475.55	03/2005 -	05/2012	86(O) -	0/0
443	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI, Uttar Pradesh	03/2005	220.00 -	220.00	272.96	09/2007 -	06/2012	57(O) -	0/0
444	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, Assam	12/2003	280.00 -	280.00	259.81	02/2009 -	03/2013	49(O) -	0/0
445	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, Assam	12/2003	196.00 -	363.74	34.23	07/2009 -	04/2014	57(O) -	0/0
446	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI, Assam	12/2003	212.00 -	386.10	21.81	09/2007 -	04/2014	79(O) -	0/0
447	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI, Karnataka	04/2000	318.00 -	207.56	180.97	08/2004 -	06/2012	94(O) -	0/0
448	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI, Karnataka	04/2000	241.00 -	196.65	171.29	08/2004 07/2010	06/2012	94(O) 23(R)	0/0
449	Hazaribagh-Ranchi - [N24000141]NHAI, Jharkhand	08/2010	625.07 -	625.07	762.49	01/2013 -	01/2013	0(O) -	0/0
450	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI, Karnataka	09/2010	946.00 -	946.00	1,241.20	- -	03/2013	- -	2/2
451	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI, Andhra Pradesh	04/2010	1,740.00 -	1,740.00	1,594.30	10/2012 -	10/2012	0(O) -	0/0
452	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI, Andhra Pradesh	08/2010	388.00 -	388.00	506.40	05/2012 -	05/2012	0(O) -	0/0
453	INDORE-DEWAS(NH-3) - [N24000159]NHAI, Madhya pradesh	11/2010	325.00 -	325.00	316.92	05/2013 -	02/2014	9(O) -	0/0
454	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI, Madhya pradesh	10/2010	1,175.00 -	1,175.00	138.67	04/2013 -	04/2013	0(O) -	0/0
455	JAIPUR-REENGUS - [N24000198]NHAI, Rajasthan	08/2010	267.81 -	267.81	358.49	02/2013 -	02/2013	0(O) -	0/0
456	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, J and K	07/2010	1,813.76 -	1,813.76	-	07/2013 -	06/2014	11(O) -	0/0
457	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI, Bihar	12/2003	340.00 -	340.00	498.63	09/2008 -	06/2012	45(O) -	0/0
458	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI, Uttar Pradesh	12/2003	355.06 -	355.06	436.86	09/2009 -	12/2012	39(O) -	0/0
459	JORBAT - BARAPANI - [N24000180]NHAI, Meghalaya	01/2011	536.00 -	536.00	357.50	01/2014 -	01/2014	0(O) -	0/0
460	Jaipur-Tonk-Deoli - [N24000135]NHAI, Rajasthan	06/2010	792.06 -	792.06	1,079.80	12/2012 -	12/2012	0(O) -	0/0
461	KOTA BYPASS, RJ-4, NH-76 (NHAI) - [240106297]NHAI, Rajasthan	12/2003	275.00 -	250.39	279.31	10/2008 -	09/2012	47(O) -	0/0

Sector Wise Details

(Apr,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
462	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00	240.00	285.56	10/2008	06/2012	44(O)	0/0
463	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,Karnataka	09/2010	671.00	671.00	737.54	-	03/2013	-	0/1
464	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00	795.00	966.77	05/2012	05/2012	0(O)	0/0
465	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI, Madhya pradesh	12/2003	407.60	407.60	185.52	06/2010	10/2012	28(O)	0/0
466	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI, Madhya pradesh	12/2003	263.17	263.17	233.77	09/2009	10/2012	37(O)	0/0
467	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI, Madhya pradesh	12/2003	225.00	225.00	261.98	10/2008	05/2012	43(O)	0/0
468	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, Assam	12/2003	155.04	280.13	85.39	11/2008	07/2013	56(O)	0/0
469	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, Assam	12/2003	199.81	385.13	48.94	04/2009	07/2013	51(O)	0/0
470	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, Assam	12/2003	167.64	167.64	6.00	11/2008	01/2014	62(O)	0/0
471	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, Assam	12/2003	200.00	200.00	96.26	04/2009	03/2013	47(O)	0/0
472	MP/Maharashtra Border-Dhula - [N24000126]NHAI, Maharashtra	12/2009	835.00	835.00	1,068.70	06/2012	06/2012	0(O)	0/0
473	MURADABAD-BAREILLY - [N24000154]NHAI, Uttar Pradesh	04/2010	1,267.00	1,267.00	1,254.70	06/2013	06/2013	0(O)	0/0
474	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, Multi State	09/2011	754.00	754.00	305.55	03/2013	03/2013	0(O)	0/0
475	Muzafarpur - Sonbarsa - [N24000174]NHAI, Bihar	05/2011	511.54	511.54	65.78	11/2013	11/2013	0(O)	0/0
476	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, Assam	12/2003	264.72	264.72	272.48	06/2008	06/2012	48(O)	0/0
477	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI, Maharashtra	03/2005	168.00	168.00	457.30	12/2008	06/2012	42(O)	0/0
478	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00	208.00	255.94	04/2008	12/2012	56(O)	0/0
479	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, Assam	12/2003	225.00	225.00	226.70	06/2008	06/2012	48(O)	0/0
480	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00	200.00	273.20	06/2008	06/2012	48(O)	0/0
481	NASHRI CHANANI - [N24000162]NHAI,J and K	06/2010	2,159.00	2,159.00	-	06/2015	06/2015	0(O)	0/0

Sector Wise Details

(Apr,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original /Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
482	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI,Karnataka	03/2005	441.00 -	441.00	958.09	- -	05/2012	- -	0/0
483	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50 363.00	363.00	248.66	06/2011 06/2011	06/2012	12(O) 12(R)	0/2
484	NH CONNECTIVITY TO ICTT VALLARPADAUE NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00 -	557.00	930.92	02/2010 -	05/2012	27(O) -	0/0
485	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,Orissa	07/2011	586.00 -	586.00	-	01/2014 -	01/2014	0(O) -	0/0
486	New 4 Lane elevated road from chennai airport - [N24000139]NHAI,Tamil Nadu	09/2010	1,655.00 -	1,655.00	393.71	09/2013 -	09/2013	0(O) -	0/0
487	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68 -	340.68	370.49	03/2008 -	06/2012	51(O) -	0/0
488	PANIKHOLI-RIMOLI - [N24000197]NHAI,Orissa	03/2012	1,410.00 -	1,410.00	78.55	09/2014 -	09/2014	0(O) -	0/0
489	PANIPAT-ROHTAK - [N24000151]NHAI,Haryana	04/2011	807.00 -	807.00	700.94	10/2014 -	10/2014	0(O) -	0/0
490	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	359.00	191.60	05/2008 -	08/2012	51(O) -	0/0
491	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,Bihar	09/2011	574.00 -	574.00	58.87	03/2014 -	03/2014	0(O) -	0/0
492	PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar	08/2010	671.30 -	671.30	501.12	02/2013 -	02/2013	0(O) -	0/0
493	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00 -	940.00	1,141.10	07/2012 -	07/2012	0(O) -	0/0
494	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55 -	1,724.55	747.77	03/2013 -	03/2013	0(O) -	0/0
495	PUNE-SHOLAPUR,Pkg-II - [N24000193]NHAI,Maharashtra	09/2011	835.00 -	835.00	-	01/2014 -	01/2014	0(O) -	0/0
496	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00 -	2,288.00	3,454.50	11/2011 -	06/2013	19(O) -	0/0
497	Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00 -	1,110.00	1,802.10	05/2012 -	05/2012	0(O) -	0/0
498	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,J and K	07/2010	1,987.00 -	1,987.00	-	07/2015 -	07/2015	0(O) -	0/0
499	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHA) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	251.03	297.84	10/2008 -	12/2012	50(O) -	0/0
500	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI,Madhya pradesh	12/2003	229.91 -	229.91	247.95	10/2008 -	09/2012	47(O) -	0/0
501	ROHTAK-BAWAL - [N24000169]NHAI,Haryana	05/2011	650.00 -	650.00	602.94	11/2013 -	11/2013	0(O) -	0/0

Sector Wise Details

(Apr,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
502	SAGAR - RAJMARG CHORAH, KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI, Madhya Pradesh	12/2003	203.43	203.43	229.13	10/2008	12/2012	50(O)	0/0
503	SAGAR BY PASS, KM 187 TO KM 211, NH-26 (NHAI) - [240106301]NHAI, Uttar Pradesh	12/2003	151.30	151.30	180.94	10/2008	05/2012	43(O)	0/0
504	SALEM - U / UNDRUPET (BOT -1/TN-06) NH -68 - [N24000102]NHAI, Tamil Nadu	03/2005	941.00	941.00	1,901.00	01/2011	05/2012	16(O)	0/0
505	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI, Gujarat	09/2010	805.39	805.39	226.74	03/2013	03/2013	0(O)	0/0
506	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI, Orissa	11/2011	909.00	909.00	-	05/2014	05/2014	0(O)	0/0
507	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, Assam	12/2003	157.47	154.57	195.52	09/2007	06/2012	57(O)	0/0
508	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, West Bengal	12/2003	225.00	225.00	180.10	07/2008	12/2012	53(O)	0/0
509	SIX LANNING OF HOSUR-KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI, Tamil Nadu	06/2011	535.00	535.00	-	12/2013	12/2013	0(O)	0/0
510	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM. - [N24000172]NHAI, Tamil Nadu	09/2011	1,250.00	1,250.00	4.93	12/2013	12/2013	0(O)	0/0
511	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI, Andhra Pradesh	11/2011	1,535.00	1,535.00	808.88	05/2014	05/2014	0(O)	0/0
512	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI, Kerala	02/2010	617.00	617.00	154.52	08/2012	10/2013	14(O)	0/0
513	SNG toBANL - [N24000189]NHAI, J and K	06/2011	1,100.70	1,100.70	-	06/2014	-	-	0/0
514	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, Assam	12/2003	245.00	245.00	491.21	03/2008	05/2012	50(O)	0/0
515	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI, Orissa	04/2000	225.00	241.53	113.73	04/2004	07/2012	99(O)	0/0
516	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI, Multi State	02/2009	1,693.75	1,693.75	2,638.80	08/2011	06/2012	10(O)	0/0
517	THANJAUR-TRICHY, NH-67 (NHAI) - [N24000056]NHAI, Tamil Nadu	03/2005	280.00	280.00	581.49	06/2009	11/2012	41(O)	0/0
518	TRICHY - KORUR NH-67 - [N24000101]NHAI, Tamil Nadu	03/2005	516.00	516.00	719.55	07/2010	03/2013	32(O)	0/0
519	Talegaon-amravati - [N24000140]NHAI, Maharashtra	11/2009	567.00	567.00	361.30	11/2013	11/2013	0(O)	0/0
520	Tirupati - Chennai - [N24000178]NHAI, Tamil Nadu	04/2011	571.00	571.00	-	10/2013	10/2013	0(O)	0/0
521	Trichy Bypass - [N24000176]NHAI, Tamil Nadu	05/2010	374.00	374.00	55.89	05/2013	05/2013	0(O)	0/0

Sector Wise Details

(Apr,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
522	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00 -	680.00	-	- -	04/2013	- -	2/2
523	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI,Uttar Pradesh	12/2003	227.00 -	227.00	383.29	12/2008 -	05/2012	41(O) -	0/0
524	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,Multi State	09/2011	2,848.00 -	2,848.00	489.89	03/2014 -	03/2014	0(O) -	0/0
525	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI,J and K	12/2003	193.09 -	166.30	184.94	03/2008 -	05/2012	50(O) -	0/0
526	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J and K	12/2003	166.27 -	193.10	161.44	03/2008 -	05/2012	50(O) -	0/0
527	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45 -	193.45	29.71	11/2012 -	11/2012	0(O) -	0/0
528	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88 -	953.88	257.83	07/2013 -	07/2013	0(O) -	0/0
529	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]NHAI,Multi State	12/2011	1,047.00 -	1,047.00	-	06/2014 -	06/2014	0(O) -	0/0
	Total		92,330.10 -	94,297.43	58,943.43				5/10
Shipping & Ports									
530	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	359.44	358.78	04/2011 06/2011	06/2012	14(O) 12(R)	0/0
531	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91 -	968.35	344.33	09/2012 -	09/2012	0(O) -	0/0
532	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 627.64	627.64	106.93	12/2012 -	12/2012	0(O) -	0/0
533	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	277.03	81.40	12/2011 08/2012	08/2012	8(O) 0(R)	0/0
534	Acquisition of two nos. of 120 B.P BY 079& 080 - [N25000042]SHIPP.,Maharashtra	04/2009	290.85 -	305.00	86.46	06/2011 06/2012	06/2012	12(O) 0(R)	0/0
535	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	994.82	189.92	02/2014 -	02/2014	0(O) -	0/0
536	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	1,028.10	371.96	12/2013 -	12/2013	0(O) -	0/0

Sector Wise Details

(Apr,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original /Revised (in months)	Milestones Achieved/ Total	
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	
537	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	743.63	12/2010 -	12/2012	24(O) -	0/0	
538	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	24(O) -	0/0	
539	CONSTRUCTION OF Berthing and Allied Facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012	22(O) -	0/0	
540	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 -	800.00	5.75	10/2008 -	10/2008	0(O) -	0/0	
541	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84 -	253.36	-	- 01/2009	01/2009	- 0(R)	0/1	
542	DEVELOPMENT OF COAL TERMINAL - [N25000055]ENNORE PORT LTD,Tamil Nadu	09/2006	399.13 -	399.13	-	08/2010 -	-	- -	0/0	
543	DEVELOPMENT OF IRON ORE TERMINAL - [N25000056]ENNORE PORT LTD,Tamil Nadu	09/2006	370.00 -	370.00	-	08/2010 -	-	- -	0/0	
544	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 600.00	600.00	67.00	03/2006 -	12/2013	93(O) -	0/0	
545	MARINE LIQUID TERMINALS - [N25000054]ENNORE TANK,Tamil Nadu	10/2004	196.25 -	196.25	-	06/2006 09/2011	09/2011	63(O) 0(R)	0/0	
546	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	29(O) -	0/0	
547	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 252.00	252.00	0.21	03/2012 -	03/2012	0(O) -	0/0	
548	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	373.22	336.26	04/2009 11/2009	02/2011	22(O) 15(R)	0/0	
549	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	2,427.40	829.14	10/2008 -	10/2008	0(O) -	0/0	
550	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	4,150.00	3,240.30	01/2012 09/2012	09/2012	8(O) 0(R)	0/0	
551	SETTING UP OF SINGLE POINT MOORING (SPM) - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -	621.53	-	05/2013 -	03/2013	-2(O) -	0/0	
Total			17,207.90	18,722.87	6,982.00					0/1

Sector Wise Details

(Apr,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original /Revised (in months)	Milestones Achieved/ Total	
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	
Telecommunications										
552	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	157.98	01/2009 -	06/2012	41(O) -	0/0	
553	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	247.00	75.89	02/2007 12/2010	08/2011	54(O) 8(R)	0/0	
554	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	229.41	67.20	02/2007 03/2011	03/2012	61(O) 12(R)	0/0	
555	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	384.00	21.93	10/2010 03/2012	07/2012	21(O) 4(R)	0/0	
556	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38 -	168.30	-	10/2007 -	-	- -	0/0	
557	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00 -	1,077.00	-	03/2009 -	-	- -	0/0	
558	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	373.94	227.29	12/2008 -	06/2012	42(O) -	0/0	
559	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 930.60	930.60	800.66	11/2010 -	03/2012	16(O) -	0/0	
560	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84 -	336.84	35.75	10/2009 -	03/2011	17(O) -	0/0	
561	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL,Jharkhandd	03/2008	328.13 -	328.12	164.58	03/2009 -	06/2012	39(O) -	0/0	
562	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	152.65	-	03/2010 -	-	- -	0/0	
563	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	952.88	-	03/2010 -	10/2010	7(O) -	0/0	
564	NIB Project Capacity Expansion - [N26000098]BSNL,Multi State	06/2007	175.52 -	175.52	60.84	12/2008 -	05/2012	41(O) -	0/0	
565	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00 -	250.00	80.47	12/2005 03/2008	05/2012	77(O) 50(R)	0/0	
566	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	158.72	76.55	06/2009 -	06/2012	36(O) -	0/0	
Total			6,161.00 -	6,101.79	1,769.14					0/0
Urban Development										
567	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00 -	11,609.00	2,267.57	12/2011 -	12/2013	24(O) -	6/6	

Sector Wise Details

(Apr,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
568	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	173.08	-	04/2009	-	-	0/0
569	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00	35,242.00	236.74	03/2016	03/2016	0(O)	0/0
570	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00	2,494.00	-	09/2014	09/2014	0(O)	0/0
	Total		44,245.18	49,518.08	2,504.31				6/6
	Water Resources								
571	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90	1,187.00	35.49	12/2007	12/2012	60(O)	0/0
	Total		542.90	1,187.00	35.49				0/0
Grand Total			733,514.85	876,715.90	392,606.54				872/2494

Sector wise current status of projects on theFlash Report

Urban Development


I. Current Status:

Number of Projects	4
Number of Projects On Schedule	2
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 2 projects are on schedule and 1 project are delayed .1 project do not have fixed dates of commissioning.

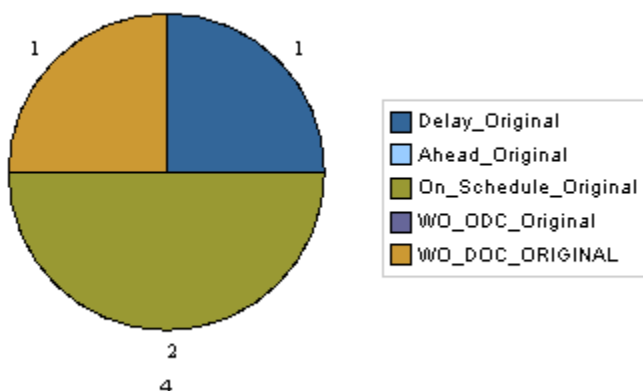

III. Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 44245.18 crore but this was subsequently revised to Rs. 49518.08 crore implying a cost overrun of 11.9%. The expenditure incurred on these projects till April, 2012 is Rs. 2504.31 crore, which is 5.1% of the revised cost of the projects.

Figures are in Rs. Crore

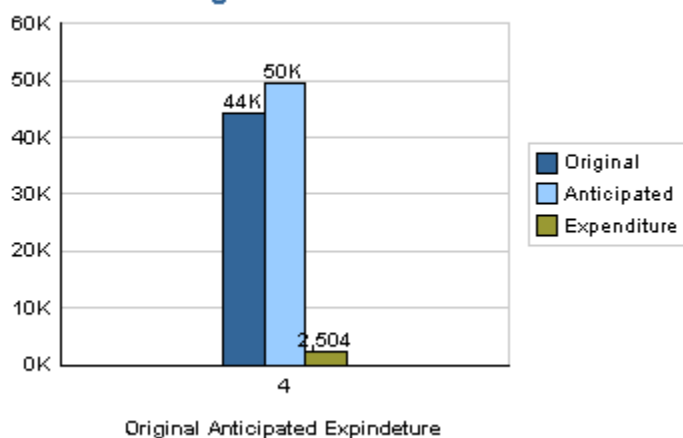

Sector wise current status of projects on theFlash Report

Telecommunications

I. Current Status:


Number of Projects **15**

Number of Projects Delayed **7**

Number of Projects Without Date Of Commissioning **8**

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 15 projects, 7 projects are delayed .8 projects do not have fixed dates of commissioning.

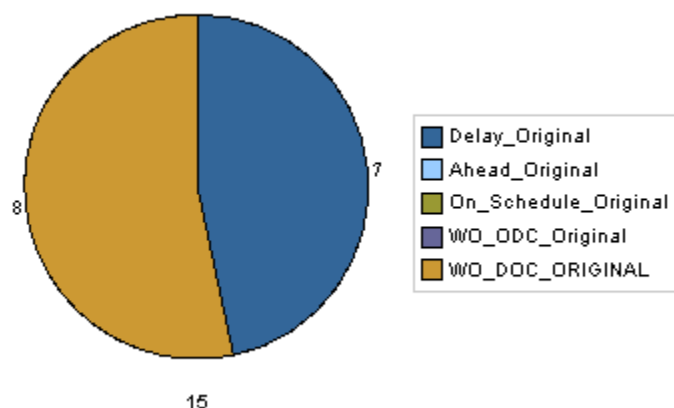

III. Investment Scenario

The Total Original cost of implementation of 15 projects when sanctioned, was of the order of Rs. 6161 crore but this was subsequently revised to Rs. 6101.79 crore implying a cost overrun of -1%. The expenditure incurred on these projects till April, 2012 is Rs. 1769.14 crore, which is 29% of the revised cost of the projects.

Figures are in Rs. Crore

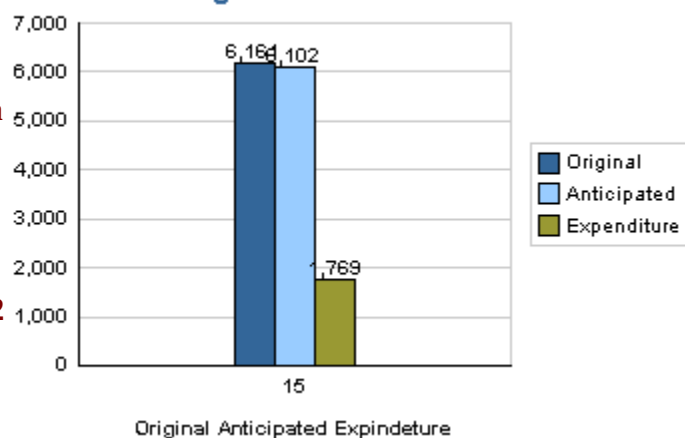

Sector wise current status of projects on theFlash Report


Shipping & Ports

I. Current Status:

Number of Projects	22
Number of Projects On Schedule	4
Number of Projects Delayed	9
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	8

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 22 projects, 1 project are ahead of schedule, 4 projects are on schedule and 9 projects are delayed .8 projects do not have fixed dates of commissioning.

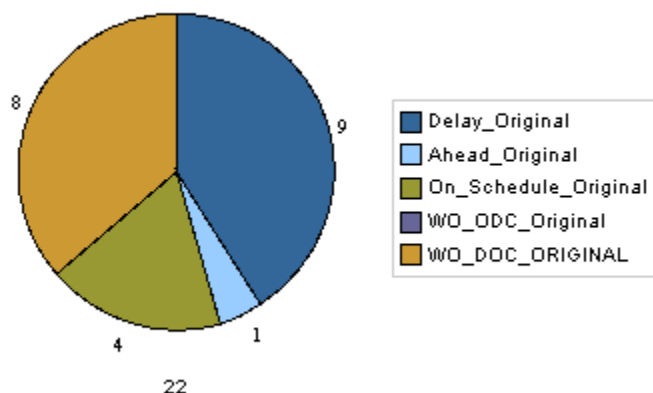

III. Investment Scenario

The Total Original cost of implementation of 22 projects when sanctioned, was of the order of Rs. 17207.9 crore but this was subsequently revised to Rs. 18722.87 crore implying a cost overrun of 8.8%. The expenditure incurred on these projects till April, 2012 is Rs. 6982 crore, which is 37.3% of the revised cost of the projects.

Figures are in Rs. Crore

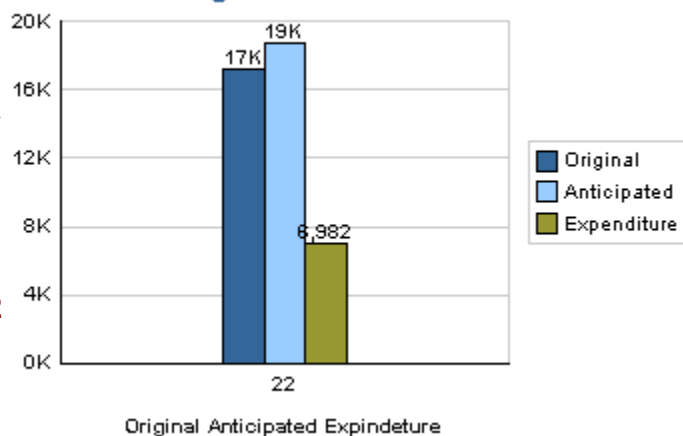

Sector wise current status of projects on theFlash Report

Road Transport & Highways


I. Current Status:

Number of Projects	148
Number of Projects On Schedule	61
Number of Projects Delayed	80

Number of Projects Without Original Date of Commissioning	7
---	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 148 projects, 61 projects are on schedule and 80 projects are delayed .7 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

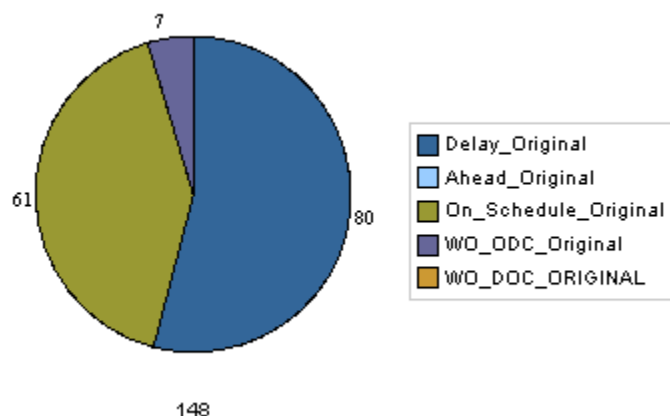

III. Investment Scenario

The Total Original cost of implementation of 148 projects when sanctioned, was of the order of Rs. 92330.1 crore but this was subsequently revised to Rs. 94297.43 crore implying a cost overrun of 2.1%. The expenditure incurred on these projects till April, 2012 is Rs. 58943.43 crore, which is 62.5% of the revised cost of the projects.

Figures are in Rs. Crore

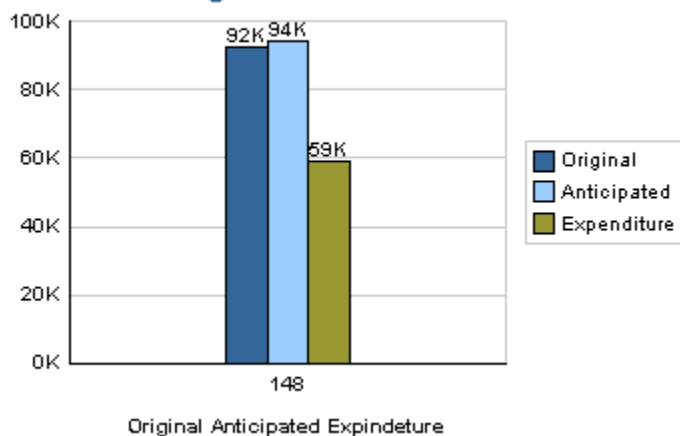

Sector wise current status of projects on theFlash Report


Railways

I. Current Status:

Number of Projects	131
Number of Projects On Schedule	17
Number of Projects Delayed	30
Number of Projects Ahead	2
Number of Projects Without Original Date of Commissioning	10
Number of Projects Without Date Of Commissioning	72

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 131 projects, 2 projects are ahead of schedule, 17 projects are on schedule and 30 projects are delayed. 72 projects do not have fixed dates of commissioning. 10 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

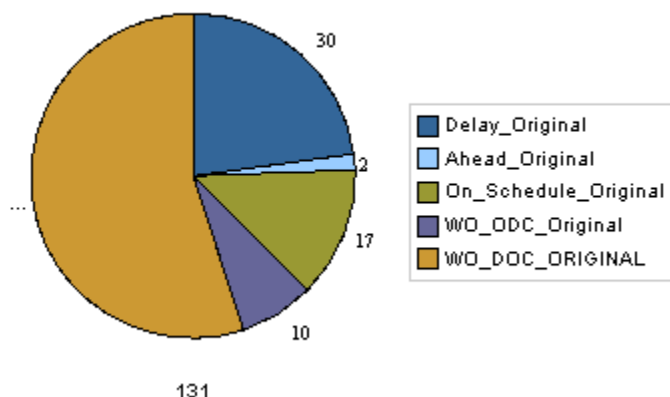

III. Investment Scenario

The Total Original cost of implementation of 131 projects when sanctioned, was of the order of Rs. 65286.3 crore but this was subsequently revised to Rs. 141884.1 crore implying a cost overrun of 117.3%. The expenditure incurred on these projects till April, 2012 is Rs. 58548.53 crore, which is 41.3% of the revised cost of the projects.

Figures are in Rs. Crore

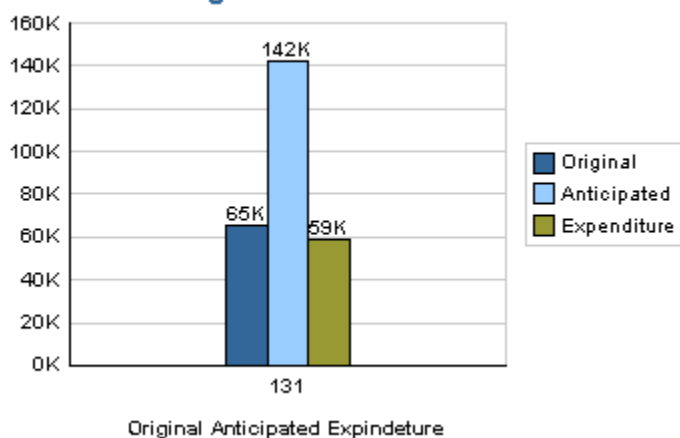

Sector wise current status of projects on theFlash Report


Power

I. Current Status:

Number of Projects	102
Number of Projects On Schedule	45
Number of Projects Delayed	51
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	2
Number of Projects Without Date Of Commissioning	3

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 102 projects, 1 project are ahead of schedule, 45 projects are on schedule and 51 projects are delayed .3 projects do not have fixed dates of commissioning.2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

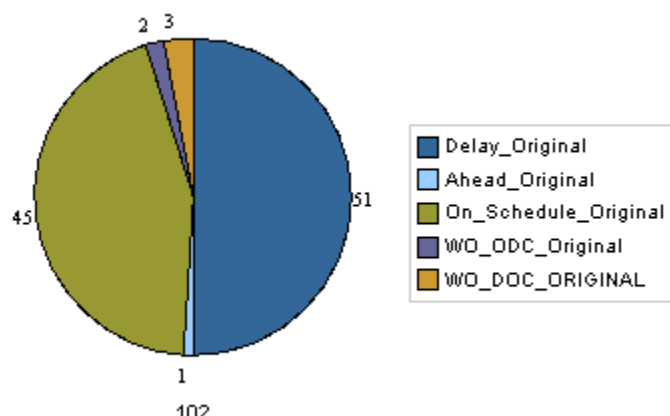

III. Investment Scenario

The Total Original cost of implementation of 102 projects when sanctioned, was of the order of Rs. 211144.68 crore but this was subsequently revised to Rs. 225276.41 crore implying a cost overrun of 6.7%. The expenditure incurred on these projects till April, 2012 is Rs. 107653.57 crore, which is 47.8% of the revised cost of the projects.

Figures are in Rs. Crore

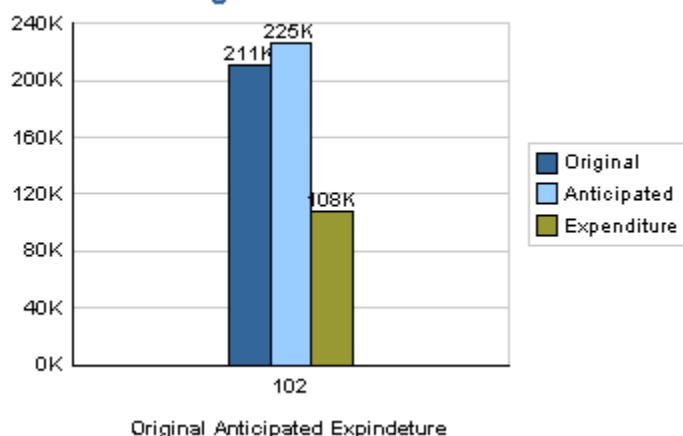

Sector wise current status of projects on theFlash Report


Petroleum

I. Current Status:

Number of Projects	64
Number of Projects On Schedule	17
Number of Projects Delayed	40
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	5

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 64 projects, 1 project are ahead of schedule, 17 projects are on schedule and 40 projects are delayed .5 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

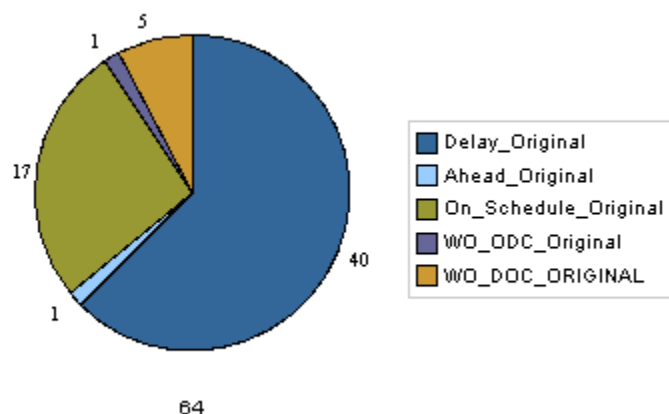

III. Investment Scenario

The Total Original cost of implementation of 64 projects when sanctioned, was of the order of Rs. 155277.97 crore but this was subsequently revised to Rs. 164778.94 crore implying a cost overrun of 6.1%. The expenditure incurred on these projects till April, 2012 is Rs. 71506.47 crore, which is 43.4% of the revised cost of the projects.

Figures are in Rs. Crore

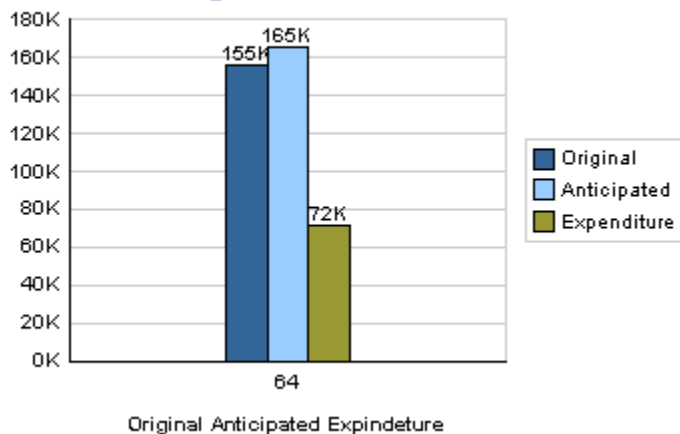

Sector wise current status of projects on theFlash Report


Steel

I. Current Status:

Number of Projects	16
Number of Projects On Schedule	2
Number of Projects Delayed	7
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	5
Number of Projects Without Date Of Commissioning	1

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 16 projects, 1 project are ahead of schedule, 2 projects are on schedule and 7 projects are delayed .1 project do not have fixed dates of commissioning.5 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

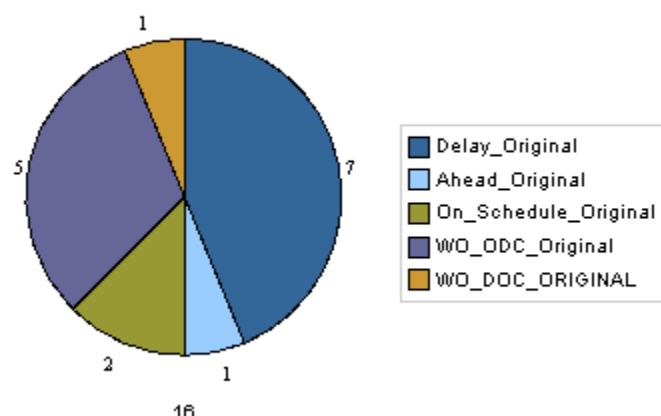

III. Investment Scenario

The Total Original cost of implementation of 16 projects when sanctioned, was of the order of Rs. 50155.82 crore but this was subsequently revised to Rs. 71402.36 crore implying a cost overrun of 42.4%. The expenditure incurred on these projects till April, 2012 is Rs. 39635.95 crore, which is 55.5% of the revised cost of the projects.

Figures are in Rs. Crore

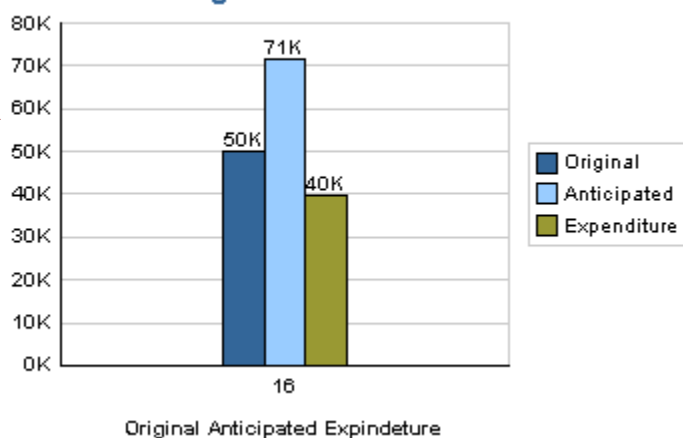

Sector wise current status of projects on theFlash Report


Fertilisers

I. Current Status:

Number of Projects	6
Number of Projects On Schedule	4
Number of Projects Delayed	2

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 6 projects, 4 projects are on schedule and 2 projects are delayed.

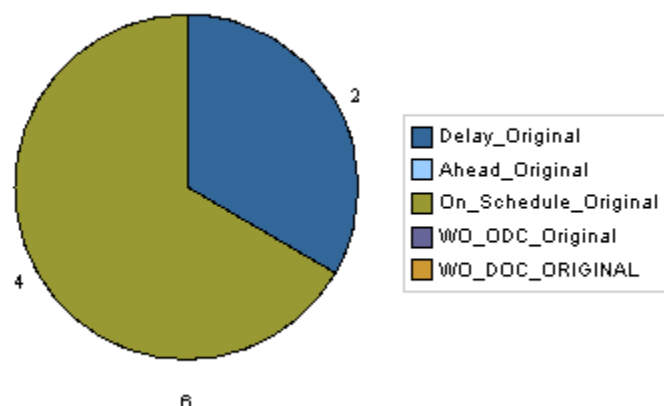

III. Investment Scenario

The Total Original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 5317.41 crore but this was subsequently revised to Rs. 5317.41 crore implying a cost overrun of 0%. The expenditure incurred on these projects till April, 2012 is Rs. 2348.53 crore, which is 44.2% of the revised cost of the projects.

Figures are in Rs. Crore

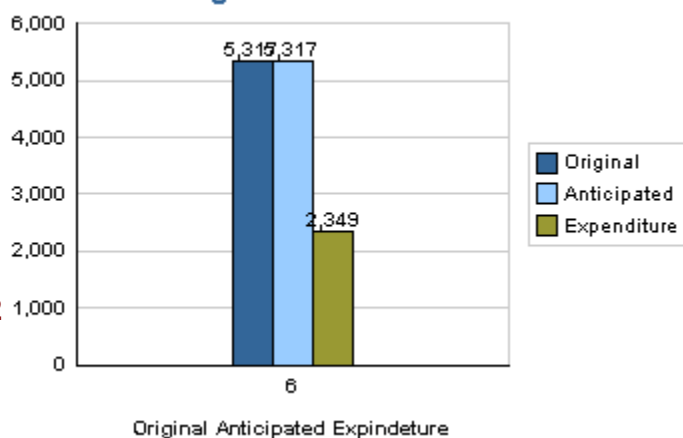

Sector wise current status of projects on theFlash Report

Coal


I. Current Status:

Number of Projects	51
Number of Projects On Schedule	21
Number of Projects Delayed	23

Number of Projects Without Original Date of Commissioning	6
Number of Projects Without Date Of Commissioning	1

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 51 projects, 21 projects are on schedule and 23 projects are delayed .1 project do not have fixed dates of commissioning.6 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

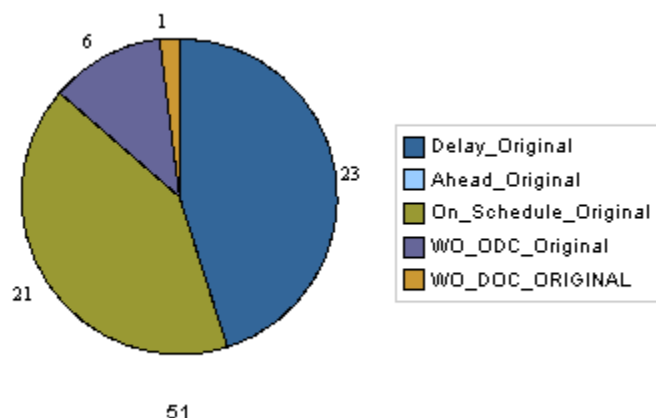

III. Investment Scenario

The Total Original cost of implementation of 51 projects when sanctioned, was of the order of Rs. 33815.11 crore but this was subsequently revised to Rs. 37312.15 crore implying a cost overrun of 10.3%. The expenditure incurred on these projects till April, 2012 is Rs. 12005.65 crore, which is 32.2% of the revised cost of the projects.

Figures are in Rs. Crore

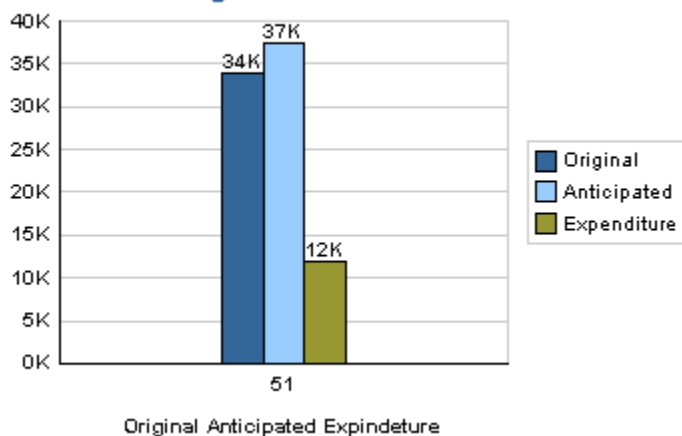

Sector wise current status of projects on theFlash Report

Civil Aviation


I. Current Status:

Number of Projects	5
Number of Projects On Schedule	1
Number of Projects Delayed	3

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 5 projects, 1 project are on schedule and 3 projects are delayed .1 project do not have fixed dates of commissioning.

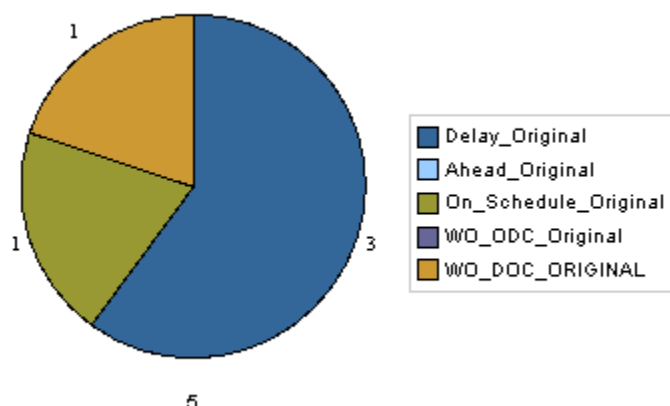

III. Investment Scenario

The Total Original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 5021.58 crore but this was subsequently revised to Rs. 5611.07 crore implying a cost overrun of 11.7%. The expenditure incurred on these projects till April, 2012 is Rs. 4219.76 crore, which is 75.2% of the revised cost of the projects.

Figures are in Rs. Crore

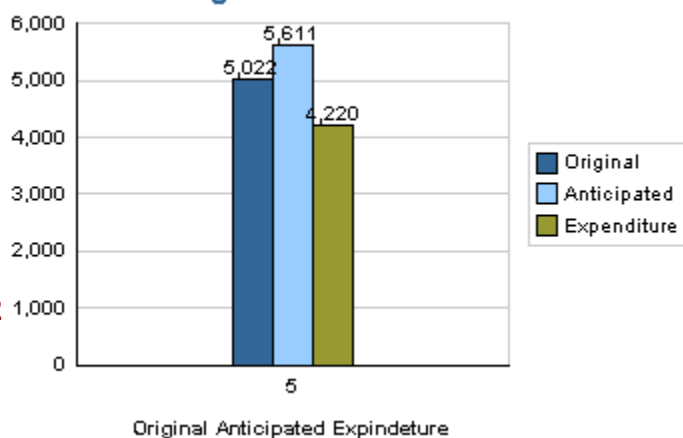

Sector wise current status of projects on theFlash Report

Atomic Energy

I. Current Status:


Number of Projects 5

Number of Projects Delayed 4

Number of Projects Without Date Of Commissioning 1

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 5 projects, 4 projects are delayed .1 project do not have fixed dates of commissioning.

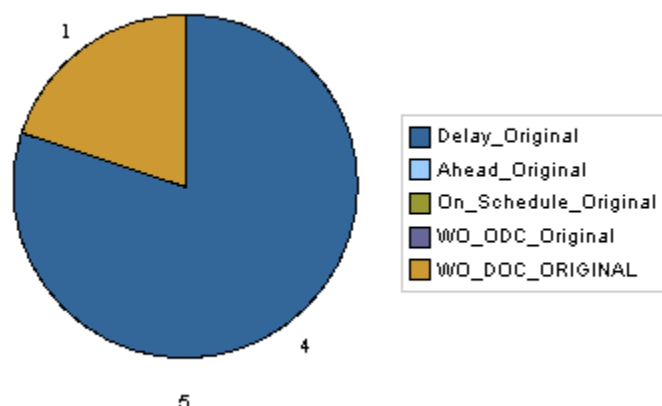

III. Investment Scenario

The Total Original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 41548.29 crore but this was subsequently revised to Rs. 46386.29 crore implying a cost overrun of 11.6%. The expenditure incurred on these projects till April, 2012 is Rs. 22118.84 crore, which is 47.7% of the revised cost of the projects.

Figures are in Rs. Crore

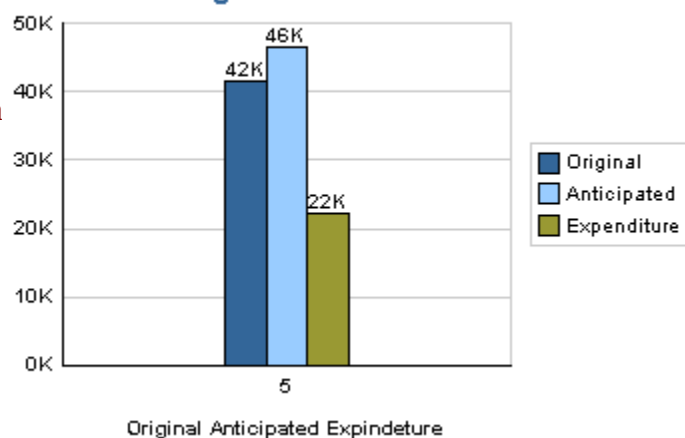

ANNEXURES

CENTRAL SECTOR PROJECTS

SN	STATE	NO OF PROJECTS	COST ORIGINAL	COS ANTICIPATED	CUMMULATIVE EXPENDITURE
1	Andhra Pradesh	36	31031.62	38459.02	20442.84
2	Arunachal Pr.	4	9512.22	14153.62	8036.96
3	Assam	37	23895.78	35736.33	22077.48
4	Bihar	32	30891.77	35948.09	23773.63
5	Chhatisgarh	26	41057.60	56554.59	20086.05
6	Delhi	3	37985.00	37965.41	303.94
7	Goa	1	335.61	335.61	105.04
8	Gujarat	24	31509.31	31737.32	6631.71
9	Haryana	10	5795.35	7611.84	7330.71
10	Himachal Pr.	6	14761.20	17455.42	13476.94
11	J and K	11	15120.05	34413.14	12870.54
12	Jharkhandd	23	11785.48	16601.53	7267.09
13	Karnataka	24	29909.64	38742.46	18095.87
14	Kerala	5	5469.67	6911.22	4758.96
15	Madhya pradesh	25	16968.45	17262.92	7867.29
16	Maharashtra	50	78548.34	93760.48	45711.32
17	Manipur	1	727.56	3056.85	738.60
18	Meghalaya	2	762.00	762.00	542.95
19	Mizoram	3	1901.69	4220.75	632.80
20	Multi State	101	133051.52	139370.06	56265.25
21	Nagaland	1	850.00	850.00	8.45
22	Orissa	30	57405.36	61206.44	26795.37
23	Punjab	6	4384.20	5314.23	3448.90
24	Rajasthan	15	26688.02	26417.90	8142.67
25	Sikkim	2	1648.94	3690.04	235.60
26	Tamil Nadu	35	52241.33	61100.42	37289.34
27	Tripura	3	1522.39	2053.23	707.17
28	Uttar Pradesh	25	18779.67	22785.21	10970.02
29	Uttaranchal	4	8514.31	9454.74	2526.07
30	West Bengal	26	40460.77	52785.03	25466.98
TOTAL		571	733514.85	876715.90	392606.54

LIST OF PROJECTS IN WHICH EXPENDITURE MORE THAN COST

SN	PROJECT	SECTOR	AGENCY	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	Atomic Energy	BHAVNI	3492.00	0.00	3641.60
2	KUDANKULAM APP (NPCIL)	Atomic Energy	NPCIL	13171.00	0.00	14714.00
3	DIPKA EXPANSION OCP (SECL) (20 MTY)	Coal	SECL	1268.53	0.00	1271.50
4	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI	Petroleum	HPCL	224.00	299.00	320.40
5	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATTNAM	Petroleum	HPCL	756.00	0.00	840.50
6	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC)	Power	NHPC	768.92	0.00	1476.77
7	TEESTA LOW DAM HEP, STAGE-IV (NHPC)	Power	NHPC	1061.38	0.00	1112.46
8	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP	Power	PGCIL	297.37	0.00	326.43
9	NIMOO BAZGO HYDROELECTRIC PROJECT	Power	NHPC	611.01	0.00	729.82
10	KUNADANKULAM-APP TRANS. SYSTEM (PGCIL)	Power	PGCIL	1779.29	0.00	1828.98
11	CHUTAK HYDRO-ELECTRIC PROJECT	Power	NHPC	621.26	0.00	733.22
12	CHAMERA,STAGE-III (NHPC)	Power	NHPC	1405.63	0.00	1815.30
13	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	Railways	NCR	158.77	432.46	558.07
14	CALICUT-MANGALORE (DL) (SR)	Railways	SR	240.00	0.00	600.41
15	KARUR-SALEM(NL),SR	Railways	SR	155.55	229.88	713.06
16	KODERMA-RANCHI VIA BARKAKANA (NL),ECR	Railways	ECR	491.19	1099.20	1223.54
17	CHANDIGARH-LUDHIANA(NEW BG LINE),NR	Railways	(NR)	248.44	576.27	989.08
18	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	Railways	NEFR	915.70	0.00	1174.67
19	KATIHAR - JOGBANI (GC)(NEFR)	Railways	NEFR	100.00	492.98	728.94
20	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	Railways	NEFR	733.00	0.00	1086.71
21	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	Railways	NCR	108.00	214.09	250.82
22	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	Railways	ECR	233.00	501.69	630.07
23	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR	Railways	NEFR	1000.00	1500.00	2387.21
24	KODERMA GIRIDH (NL), ECR	Railways	ECR	371.36	0.00	402.20
25	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	ECOR	100.00	142.98	200.21
26	MUMBAI URBAN TRANSPORT PROJECT PHASE-I	Railways	M RTP	3125.20	4174.40	4334.00
27	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	Railways	ECR	114.01	332.92	378.14

SN	PROJECT	SECTOR	AGENCY	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
28	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	Railways	SR	343.17	0.00	505.61
29	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSION	Railways	RVNL	200.80	0.00	269.02
30	REWARI-ROHTAK (NL),NR	Railways	(NR)	149.38	330.23	519.90
31	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	Railways	(NR)	409.00	625.30	854.37
32	KAPTANGANJ-THANE-SIWAN-CHHAPRA GC (NER)	Railways	NER	323.40	0.00	474.97
33	KANPUR-KASGANJ-MATHURA(GC),NER	Railways	NER	395.00	1062.36	1255.66
34	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project	Railways	NEFR	1676.31	0.00	3055.16
35	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR	Railways	NEFR	156.00	0.00	240.26
36	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	Railways	NEFR	170.00	0.00	392.90
37	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	Railways	NEFR	727.56	0.00	738.60
38	RAJPIPLA-ANKELASHWAR, WR (GC)	Railways	WR	196.97	0.00	213.97
39	AMRAVATI-NARKHER NL(CR)	Railways	CR	120.90	284.27	516.67
40	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	SCR	124.43	495.68	557.79
41	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	Railways	SR	100.00	0.00	495.87
42	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR	Railways	SWR	295.00	412.91	483.14
43	KOTTUR-HARIHAR(NL),(SWR)	Railways	SWR	65.94	302.23	331.25
44	RANCHI-LOHARDAGA(GC),SER	Railways	SER	194.07	0.00	281.69
45	NANDYAL-YERRAGUNTALA(NL),SCR	Railways	SCR	155.74	429.49	583.44
46	ELECTRIFICATION OF MORADABAD-ROZA	Railways	RE	129.17	0.00	227.48
47	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER)	Railways	NER	381.17	0.00	509.13
48	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara and Noapara-NSCB Airport(MTP)	Railways	MRTP	907.69	3176.10	3183.24
49	GADWAL - RAICHUR (NL), SCR	Railways	SCR	92.63	228.09	258.21
50	JIND-SONEPAT (NL),NR	Railways	(NR)	190.81	238.56	559.46
51	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402	Road Transport & Highways	NHAI	240.00	0.00	285.56
52	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	Road Transport & Highways	NHAI	157.47	0.00	195.52
53	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2)	Road Transport & Highways	NHAI	367.49	0.00	453.68
54	HALDIA PORT (PORT CONNECTIVITY) (NH-41)	Road Transport & Highways	NHAI	273.00	0.00	475.55

SN	PROJECT	SECTOR	AGENCY	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
55	Armur to kadloor yellareddy	Road Transport & Highways	NHAI	390.56	0.00	631.65
56	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA	Road Transport & Highways	NHAI	229.91	0.00	247.95
57	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI)	Road Transport & Highways	NHAI	203.43	0.00	229.13
58	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI)	Road Transport & Highways	NHAI	151.30	0.00	180.94
59	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI)	Road Transport & Highways	NHAI	225.00	0.00	261.98
60	JHANSI TO LALITPUR, NH-25,26	Road Transport & Highways	NHAI	355.06	0.00	436.86
61	KOTA BYPASS,RJ-4, NH-76 (NHAI)	Road Transport & Highways	NHAI	275.00	0.00	279.31
62	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0	Road Transport & Highways	NHAI	340.68	0.00	370.49
63	JHAJHARPUR TO DARBANGA (BR-7)	Road Transport & Highways	NHAI	340.00	0.00	498.63
64	JAIPUR-REENGUS	Road Transport & Highways	NHAI	267.81	0.00	358.49
65	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVIHALLI	Road Transport & Highways	NHAI	441.00	0.00	958.09
66	KUNDUPUR-SURATHKAL & MANGLORE	Road Transport & Highways	NHAI	671.00	0.00	737.54
67	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	Road Transport & Highways	NHAI	237.80	0.00	238.58
68	4 LANNING OF AHMEDABAD TO GODHARA	Road Transport & Highways	NHAI	1008.50	0.00	1079.10
69	Hungund-Surathkal and Mangalore-Knt/Kerala Border	Road Transport & Highways	NHAI	946.00	0.00	1241.20
70	NH CONNECTIVITY TO ICTT VALLARPADAEU NH - SH	Road Transport & Highways	NHAI	557.00	0.00	930.92

SN	PROJECT	SECTOR	AGENCY	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
71	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.15)	Road Transport & Highways	NHAI	572.30	0.00	647.98
72	Surat- Dahisar(Six Lane) Km 263 to Km 502	Road Transport & Highways	NHAI	1693.75	0.00	2638.80
73	Gurgaon-Kotputli Km 42.70 to 54.4 Km	Road Transport & Highways	NHAI	1673.70	0.00	2406.10
74	TRICHY - KORUR NH-67	Road Transport & Highways	NHAI	516.00	0.00	719.55
75	THANJAUR-TRICHY,NH-67(NHAI)	Road Transport & Highways	NHAI	280.00	0.00	581.49
76	SALEM - U / UNDRUPET(BOT -1/TN-06) NH - 68	Road Transport & Highways	NHAI	941.00	0.00	1901.00
77	Jaipur-Tonk-Deoli	Road Transport & Highways	NHAI	792.06	0.00	1079.80
78	AMRITSAR-PATHANKOT	Road Transport & Highways	NHAI	705.00	0.00	935.59
79	Pune-sholapur,pkg1	Road Transport & Highways	NHAI	1110.00	0.00	1802.10
80	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	Road Transport & Highways	NHAI	940.00	0.00	1141.10
81	MP/Maharashtra Border-Dhula	Road Transport & Highways	NHAI	835.00	0.00	1068.70
82	Hazaribagh-Ranchi	Road Transport & Highways	NHAI	625.07	0.00	762.49
83	AURANG-RAIPUR, NH-6, KM.232 TO KM.281	Road Transport & Highways	NHAI	190.00	0.00	254.19
84	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER	Road Transport & Highways	NHAI	464.00	0.00	534.79
85	GANJAM-ICCHAPURUM,NH-5(NHAI)	Road Transport & Highways	NHAI	263.27	0.00	265.81
86	ASSAM/WB BORDER TO GAIRKATTA (WB-1)	Road Transport & Highways	NHAI	221.82	0.00	278.86

SN	PROJECT	SECTOR	AGENCY	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
87	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	Road Transport & Highways	NHAI	195.00	0.00	196.85
88	NALBARI TO BIJNI (AS-8)	Road Transport & Highways	NHAI	200.00	0.00	273.20
89	NALBARI TO BIJNI (AS-6)	Road Transport & Highways	NHAI	225.00	0.00	226.70
90	NALBARI T BIJNI (AS-7)	Road Transport & Highways	NHAI	208.00	0.00	255.94
91	SONAPUR TO GUWAHTI (AS-3)	Road Transport & Highways	NHAI	245.00	0.00	491.21
92	DHARAMTUL TO SONAPUR (AS-19)	Road Transport & Highways	NHAI	200.00	0.00	209.81
93	NAGAON TO DHARAMTUL (AS-2)	Road Transport & Highways	NHAI	264.72	0.00	272.48
94	GUWAHATI TO NALBARI (AS-5)	Road Transport & Highways	NHAI	198.16	0.00	202.60
95	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km)	Road Transport & Highways	NHAI	1108.00	0.00	3454.50
96	Kishangarh-Ajmer-Beawer	Road Transport & Highways	NHAI	795.00	0.00	966.77
97	Hyderabad-yadgiri N.H no-202	Road Transport & Highways	NHAI	388.00	0.00	506.40
98	NAGPUR-KONDHALI,NH-6(NHAI)	Road Transport & Highways	NHAI	168.00	0.00	457.30
99	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	Road Transport & Highways	NHAI	232.45	0.00	251.79
100	GWALIOR BYPASS, NH-75,3	Road Transport & Highways	NHAI	300.93	0.00	302.72
101	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	Road Transport & Highways	NHAI	332.94	0.00	357.43
102	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI)	Road Transport & Highways	NHAI	251.03	0.00	297.84

SN	PROJECT	SECTOR	AGENCY	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
103	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI)	Road Transport & Highways	NHAI	227.00	0.00	383.29
104	DAKOBA TO NAGAON (NH-36)(NHAI)	Road Transport & Highways	NHAI	225.00	0.00	267.44
105	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	Road Transport & Highways	NHAI	160.00	0.00	164.32
106	DELHI/ HARYANA BORDER TO ROHTAK	Road Transport & Highways	NHAI	486.00	0.00	577.73
107	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24	Road Transport & Highways	NHAI	275.00	0.00	304.24
108	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24	Road Transport & Highways	NHAI	220.00	0.00	272.96
109	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	Shipping & Ports	RVNL	245.67	298.17	336.26
110	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREMENT EXP. UNIT	Steel	RINL	230.00	0.00	246.84

Ahead of schedule

S.No	Project	DOA	DOC Original	DOC Revised	DOC Anticipated	COST Original	Cost Anticipated
1	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY	3/2009	09/2012	05/2012	05/2012	3284	2174
2	BHAIRABI SAIRONG, NL, NEFR	4/2008	04/2014	N.A.	03/2014	619.34	2393.49
3	MAUDA TRANSMISSION SYSTEM	2/2010	10/2012	N.A.	05/2012	469.38	469.38
4	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS	2/2011	05/2013	N.A.	03/2013	830	621.53
5	CHURCHGATE-VIRAR CONV.OF 1500V DC TRACTION TO 25 KV AC,WR	7/1996	06/2013	06/2012	06/2012	653.84	1302.12
6	EXPENSION OF ROURKELA STEEL PLANT	9/2008	11/2013	N.A.	03/2013	11812	11812

List of project Without Original Date of Commissioning

(Apr,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>Coal</u>								
1	KUSMUNDA EXPN.OCP(SECL)(10-15MTY) - [N06000008]SECL,Chhatisgarh	06/2006	737.65 -	1,188.31	683.58	- 03/2013	03/2013	0(R3)	0/8
2	CHURCHA ROUG (1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35 -	462.35	272.54	- 03/2014	03/2014	0(R3)	0/7
3	KARTALI (EAST) OCP(2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44 -	178.44	-	- -	03/2014	-	0/6
4	MANIKPUR OC EXPANTION (3.50 MTY) - [N06000081]SECL,Chhatisgarh	11/2009	321.42 -	321.50	210.36	- 03/2014	03/2014	0(R3)	0/5
5	JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh	09/2008	152.43 -	152.43	-	- -	03/2015	-	0/6
6	AMLAI OC EXPANSION SECTOR 1.50 MTY - [N06000082]SECL,Chhatisgarh	11/2009	150.59 -	198.59	95.25	- -	03/2016	-	0/6
	Total		2,002.88 -	2,501.62	1,261.73				0/38
	<u>Steel</u>								
7	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhandd	01/2008	3,316.00 -	6,325.00	2,624.65	- -	10/2012	-	3/16
8	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00 16,408.00	16,408.00	13,087.79	- -	12/2012	-	7/19
9	1.2 MTPA PELLET PLANT DONIMALAI - [N12000072]NMDC,Karnataka	04/2011	572.00 -	572.00	-	- -	04/2013	-	0/19
10	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	5,185.00 -	17,265.00	5,179.68	- -	09/2013	-	9/27
11	ENHANCEMENT OF PROD. CAP. AT BOLANI I/O MINES - [N12000075]SAIL,Orissa	11/2011	254.55 -	254.55	5.54	- -	11/2013	-	0/1
	Total		23,770.55 -	40,824.55	20,897.66				19/82
	<u>Petroleum</u>								
12	CDU/VDU-II - [N16000110]CPCL,Tamil Nadu	03/2010	333.99 -	333.99	120.71	- -	09/2012	-	23/36
	Total		333.99 -	333.99	120.71				23/36
	<u>Power</u>								
13	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 623.44	623.44	185.78	- 07/2013	07/2013	0(R3)	0/29
14	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	3,065.00	- -	11/2014	-	4/28
	Total		4,796.36 -	4,998.79	3,250.78				4/57

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
Railways									
15	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 514.68	2,200.00	150.56	- -	06/2012	-	0/0
16	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	182.36	- -	03/2013	-	0/0
17	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	1,029.00	733.51	- -	03/2013	-	0/0
18	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 -	1,717.29	1,174.67	- -	03/2013	-	0/0
19	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	810.78	109.94	- -	03/2013	-	0/0
20	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	194.91	- -	12/2013	-	0/0
21	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 -	384.04	97.57	- -	03/2014	-	0/0
22	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	703.17	240.74	- -	03/2015	-	0/0
23	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	324.66	177.81	- -	03/2015	-	0/0
24	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 -	359.86	1.22	- -	03/2015	-	0/0
	Total		3,655.75 -	8,524.81	3,063.29				0/0
Road Transport & Highways									
25	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI,Karnataka	03/2005	441.00 -	441.00	958.09	- -	05/2012	-	0/0
26	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI,Karnataka	09/2010	946.00 -	946.00	1,241.20	- -	03/2013	-	2/2
27	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,Karnataka	09/2010	671.00 -	671.00	737.54	- -	03/2013	-	0/1
28	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00 -	680.00	-	- -	04/2013	-	2/2
29	DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka	12/2010	453.00 -	453.00	239.98	- -	06/2013	-	1/1
30	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka	12/2010	480.00 -	480.00	331.15	- -	10/2013	-	0/1
31	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,Karnataka	03/2011	839.00 -	839.00	56.04	- -	12/2013	-	0/1
	Total		4,510.00 -	4,510.00	3,564.00				5/8
Grand Total			39,069.53	61,693.76	32,158.17				51/221

List of project Without Date of Commissioning

Date of Commissioning					
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
<u>Atomic Energy</u>					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00	09/2010	01/2012
	Total		3,492.00		
<u>Civil Aviation</u>					
2	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00	01/2011	02/2012
	Total		1,808.00	02/2012	
<u>Coal</u>					
3	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03	03/2012	03/2012
	Total		249.03		
<u>Steel</u>					
4	Rebuilding of coke oven battery No.1 and 2 (Bokar - [N12000033]SAIL,Jharkhandd	10/2007	500.90	-	02/2012
	Total		500.90		
<u>Petroleum</u>					
5	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00	09/2011	03/2012
6	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00	02/2011	08/2011
7	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00	-	-
8	EURO-IV DHDT - [N16000109]CPCL,Tamil Nadu	09/2008	2,615.69	-	-
9	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON - [N16000009]BRPL,Assam	06/2006	1,431.91	09/2009	-
	Total		6,611.60		
<u>Power</u>					
10	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45	12/2007	12/2009
11	KUDANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29	09/2008	-
12	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69	09/2010	-
	Total		2,853.43		

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>Railways</u>				
13	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	03/1998 -	03/1998
14	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	04/2003 03/2010	03/2010
15	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	06/2008
16	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhand	03/1999	491.19 1,099.20	07/2005 -	07/2005
17	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94 604.04	03/1998 08/2005	08/2005
18	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30	06/2007 -	06/2007
19	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	07/2008 -	07/2008
20	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	- 05/2009	05/2009
21	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 3,176.10	12/2006 08/2010	08/2010
22	BELAPUR-SEAWOOD-URAN ELECTRIF-IED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	03/2004 12/2010	12/2010
23	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	12/2010
24	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL,Uttar Pradesh	04/2003	230.73 399.73	03/2009 12/2008	12/2010
25	Pandabeswar-Chinpa doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 293.74	12/2010 12/2010	12/2010
26	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	02/2010 02/2011	02/2011
27	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	06/1999 03/2011	03/2011
28	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	- -	03/2011
29	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	05/2008 03/2011	03/2011
30	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	12/2009 03/2011	03/2011
31	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/2001	143.92 258.60	03/2011 03/2011	03/2011
32	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	- 03/2009	03/2011
33	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 -	03/2009 12/2009	03/2011
34	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 -	03/2011 03/2011	03/2011
35	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011
36	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	03/2011 -	03/2011
37	MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N22000093]MRTP,Maharashtra	04/2003	3,125.20 4,174.40	06/2011 06/2011	06/2011
38	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100007]NCR,Multi State	04/1985	158.77 432.46	03/1994 -	12/2011

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
39	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 1,185.00	- 09/2009	12/2011
40	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	- -	02/2012
41	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	- -	02/2012
42	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	- 12/2009	02/2012
43	Dakshin-barasal-lakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	12/2011 02/2012	02/2012
44	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	- -	03/2012
45	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.98	03/2002 -	03/2012
46	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 900.05	12/2011 12/2011	03/2012
47	KADUR-CHIKMAGALUR-SAKLIESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	03/2012 03/2012	03/2012
48	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	02/2009 -	03/2012
49	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	- -	03/2012
50	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	03/2012 03/2012	03/2012
51	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	02/2011 02/2011	03/2012
52	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	- -	03/2012
53	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	03/2012 03/2012	03/2012
54	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	- -	03/2012
55	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	- -	03/2012
56	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	03/2010 -	03/2012
57	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 -	- -	03/2012
58	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	03/2012 -	03/2012
59	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	03/2011 -	03/2012
60	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand	04/2008	167.73 -	03/2012 -	03/2012
61	Bhuj-Naliya(GC) with extension from naliyate vayor - [N22000123]WR,Gujarat	04/2008	318.24 -	03/2012 -	03/2012
62	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	- 03/2010	-
63	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	- -	-
64	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 229.88	- -	-
65	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00 -	- -	-

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
66	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00	-	-
			-	-	
67	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23	-	-
			162.87	-	
68	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00	-	-
			-	-	
69	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00	-	-
			1,045.00	-	
70	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00	-	-
			-	-	
71	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91	-	-
			418.17	-	
72	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13	-	-
			727.13	-	
73	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56	-	-
			671.82	-	
74	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' -A - [N22000079]SR,Tamil Nadu	09/2007	404.19	-	-
			-	-	
75	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17	-	-
			-	-	
76	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN - [N22000081]RVNL,Gujarat	09/2005	200.80	-	-
			-	-	
77	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00	-	-
			-	-	
78	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00	-	-
			582.83	-	
79	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00	-	-
			-	-	
80	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17	-	-
			-	-	
81	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40	-	-
			-	-	
82	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd	04/1996	371.36	-	-
			-	-	
83	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19	-	-
			-	-	
84	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03	-	-
			-	-	
Total			22,119.72		
			-		
<u>Shipping & Ports</u>					
85	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40	10/2008	10/2008
			-	-	
86	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00	10/2008	10/2008
			-	-	
87	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84	-	01/2009
			-	01/2009	
88	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67	04/2009	02/2011
			298.17	11/2009	
89	MARINE LIQUID TERMINALS - [N25000054]ENNORE TANK,Tamil Nadu	10/2004	196.25	06/2006	09/2011
			-	09/2011	
90	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00	03/2012	03/2012
			252.00	-	

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
91	DEVELOPMENT OF COAL TERMINAL - [N25000055]ENNORE PORT LTD,Tamil Nadu	09/2006	399.13 -	08/2010 -	-
92	DEVELOPMENT OF IRON ORE TERMINAL - [N25000056]ENNORE PORT LTD,Tamil Nadu	09/2006	370.00 -	08/2010 -	-
	Total		4,870.29 -		
<u>Telecommunications</u>					
93	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	03/2010 -	10/2010
94	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84 -	10/2009 -	03/2011
95	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	02/2007 12/2010	08/2011
96	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	02/2007 03/2011	03/2012
97	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 930.60	11/2010 -	03/2012
98	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38 -	10/2007 -	-
99	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00 -	03/2009 -	-
100	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	03/2010 -	-
	Total		4,163.45 -		
<u>Urban Development</u>					
101	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	04/2009 -	-
	Total		114.18 -		
Grand Total			46,782.60		

List of On Schedule

S.No	Project	DOA	DOC Original	DOC Revised	DOC Anticipated	COST Original	Cost Anticipated
1	CHANDIGARH- LUDHIANA(NEW BG LINE),NR	7/1998	12/2012	N.A.	12/2012	248.44	1103.47
2	DEOGHAR - SULTANGANJ (INL), ER	4/2000	12/2012	12/2012	12/2012	138	607.09
3	SUKINDA ROAD - ANGUL (NL)(ECOR)	4/1998	02/2015	N.A.	02/2015	183.23	818.29
4	JAGANNATHPOR OC	9/2008	03/2015	N.A.	03/2015	152.43	152.43
5	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA MEGA POWER PROJECT	12/2008	12/2012	N.A.	12/2012	7031.88	7031.88
6	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGEVER PROJECT	1/2010	01/2013	N.A.	01/2013	1294.19	1294.19
7	Talegaon-amravati	11/2009	11/2013	N.A.	11/2013	567	567
8	Hyderabad-yadgiri N.H no-202	8/2010	05/2012	N.A.	05/2012	388	388
9	Purnadih OCP	7/2008	03/2013	N.A.	03/2013	210.98	210.98
10	IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS	2/2010	06/2012	N.A.	06/2012	215.86	215.86
11	KARMA OCP	6/2009	03/2014	N.A.	03/2014	162.46	162.46
12	THAL AMMONIA REVAMP PROJECT	1/2009	04/2012	04/2012	04/2012	488.75	488.75
13	Kishangarh-Ajmer-Beawer	11/2009	05/2012	N.A.	05/2012	795	795
14	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C	3/2011	03/2014	N.A.	03/2014	2569.25	2569.25
15	Hyderabad-Vijaywada Km. 40 to 221.50 Km	4/2010	10/2012	N.A.	10/2012	1740	1740
16	New Work for Construction of Metro railway from Joka to Binoy Badal Dinesh Bagh.	4/2010	03/2016	N.A.	03/2016	2619.02	2619.02
17	Jaipur - Ringus - Churu and Sikar - Loharu Guage Conversion (NWR)	4/2008	03/2014	N.A.	03/2014	653.19	653.46
18	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII	12/2010	08/2013	N.A.	08/2013	209.78	209.78
19	Transmission system for transfer	3/2011	11/2013	N.A.	11/2013	1585.12	1585.12

	of power from Gen.proj in sikkim to NR/WR part-B						
20	Ahmedabad Redevelopment	11/2010	12/2014	N.A.	12/2014	1916.1	1916.1
21	DEOLI-KOTA	1/2011	07/2013	N.A.	07/2013	953	593
22	JALLARAM SHAFT PROJECT	3/2013	03/2013	N.A.	03/2013	467.78	467.78
23	Batura OCP (2.0 MTY)	9/2008	03/2015	N.A.	03/2015	203.82	203.82
24	Kistaram OCP	11/2010	03/2015	N.A.	03/2015	242.29	242.29
25	PELMA OCP(10.00MTY)	7/2008	03/2015	N.A.	03/2015	448.32	448.32
26	KARTALI (EAST) OC	7/2008	03/2014	N.A.	03/2014	178.44	178.44
27	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	11/2009	03/2016	N.A.	03/2016	150.59	198.59
28	System Strengthening -X of SR	12/2009	04/2012	N.A.	04/2012	276.61	276.61
29	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM BHU	4/2010	01/2015	N.A.	01/2015	4404.57	4404.57
30	Establishment of pooling stations at Rajgarh and raipur for IPP generation projects in chattisgarh	12/2010	08/2013	N.A.	08/2013	1719.52	1719.52
31	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX	10/2010	01/2013	N.A.	01/2013	182.68	182.68
32	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-PART A	9/2010	03/2013	N.A.	03/2013	2074.86	2074.86
33	Polypropylene unit	5/2009	07/2012	N.A.	07/2012	1803.78	1803.78
34	Development of WO-16 Cluster Fields	6/2010	01/2014	N.A.	01/2014	2523	2523
35	Ankleswar Redevelopment	11/2010	12/2014	N.A.	12/2014	2189.63	2189.63
36	Mehesana Redevelopment	11/2010	04/2015	N.A.	04/2015	3823	3823
37	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA	8/2010	02/2014	N.A.	02/2014	8140	8140
38	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN ORISSA-B	12/2010	12/2013	N.A.	12/2013	2743.19	2743.19
39	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM PART A	12/2010	08/2013	N.A.	08/2013	779.21	779.21
40	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	4/2006	06/2013	06/2013	06/2013	495.74	495.74
41	New Line from Dimapur to Zubza(Kohima) national project (NEFR)	4/2006	03/2015	N.A.	03/2015	850	850

42	AGARTALA SABROOM, NL, NEFR	4/2008	03/2014	N.A.	03/2014	813.34	1141.75
43	SEVOK RANGPO, NEFR	4/2008	12/2015	N.A.	12/2015	1339.48	3380.58
44	Suratpura - Hanumangarh - Sriganganagar Guage Conversion (NWR)	4/2008	03/2014	N.A.	03/2014	516.23	516.23
45	NANGALDAM- TALWARA(NL),NR	3/1981	07/2012	07/2012	07/2012	37.68	730
46	DALLI-RAJHARA - RAOGHAT(PART OF DALLI- RAJHARA- JAGDALPUR),NL,RVNL	4/1995	12/2012	N.A.	12/2012	304	968.6
47	New Work for Construction of Metro railway from NSCB Airport to New Garia VIA Rajarhat (MTP)	4/2010	03/2016	N.A.	03/2016	3951.98	3951.98
48	Ramanagram-Mysore doubling with electrification of Kengesii- Musore (SWR)	4/2007	03/2013	N.A.	03/2013	482	482.7
49	Udhna-Jalgaon with electrification(doubling) (WR)	4/2008	03/2014	N.A.	03/2014	1389.62	1389.62
50	Ahmedabad-Himmatnagar- Udaipur (WR)	4/2008	03/2013	N.A.	03/2013	394.14	394.14
51	7.0 MTPA KUMARASWAMY IRON ORE MINE	2/2011	05/2013	N.A.	05/2013	898.55	898.55
52	WADNER-DEVDHARI(NS- 60/MH)(KM 94-123 KM)	2/2011	11/2012	N.A.	11/2012	193.45	193.45
53	PANIPAT-ROHTAK	4/2011	10/2014	N.A.	10/2014	807	807
54	MURADABAD-BAREILY	4/2010	06/2013	N.A.	06/2013	1267	1267
55	4 LANING OF NAGPUR- BETUL	2/2011	08/2014	N.A.	08/2014	2498.76	2498.76
56	PUNE-SATARA(NH-4)	10/2010	03/2013	N.A.	03/2013	1724.55	1724.55
57	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH	5/2011	05/2014	N.A.	05/2014	1961.87	1961.87
58	CHENGAPALLI TO COIMBATORE BYPASS KM- 102.035-144.740 KM	9/2010	03/2013	N.A.	03/2013	852	852
59	CUDDAPAH-MYDUKUR- KURNOOL KM-167.750- 356.502 KM	11/2010	05/2013	N.A.	05/2013	1585	1585
60	Gujarat/Maharashtra BorderSurat-Hazira Port Section	3/2010	09/2012	N.A.	09/2012	1509.1	1509.1
61	Hazaribagh-Ranchi	8/2010	01/2013	N.A.	01/2013	625.07	625.07
62	Indore-Jhabua-Gujrat/MP	10/2010	04/2013	N.A.	04/2013	1175	1175

63	MP/Maharashtra Border-Dhula	12/2009	06/2012	N.A.	06/2012	835	835
64	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	3/2005	07/2012	N.A.	07/2012	940	940
65	Pune-sholapur, pkg1	11/2009	05/2012	N.A.	05/2012	1110	1110
66	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI	7/2010	07/2013	N.A.	07/2013	752.64	752.64
67	Jaipur-Tonk-Deoli	6/2010	12/2012	N.A.	12/2012	792.06	792.06
68	Transmission system for transfer of power from Gen.proj in sikkim to NR/WR part-A	5/2010	01/2013	N.A.	01/2013	250.03	250.03
69	New 4 Lane elevated road from chennai airport-maduravoyal NH no.4	9/2010	09/2013	N.A.	09/2013	1655	1655
70	System Strengthening -XII of SR	2/2010	06/2012	N.A.	06/2012	232.34	232.34
71	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR TPS	8/2010	04/2013	N.A.	04/2013	170.36	170.36
72	Wax Project	6/2010	12/2013	12/2013	12/2013	576.6	576.6
73	KUSMUNDA EXPN.OCP(SECL)(10MTY)	6/2006	03/2013	03/2013	03/2013	737.65	1188.31
74	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJECT	1/2010	01/2013	N.A.	01/2013	1292.84	1292.84
75	DELHI MRTS PHASE-III	9/2011	03/2016	N.A.	03/2016	35242	35242
76	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CARRIERS	8/2008	09/2012	N.A.	09/2012	1066.91	968.35
77	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers from M/S Jiangsu Eastern Heavy Industries	8/2010	12/2012	N.A.	12/2012	612.72	627.64
78	Acquisition of two(2) Nos. of 317000 DWT very large crude carriers from M/S Jiangsu rongsheng heavy	10/2010	02/2014	N.A.	02/2014	966.46	994.82
79	Acquistion of three(3) nos of 6500TEU Cellular container vessels from M/S stx shipbuilding co. ltd.	10/2010	12/2013	N.A.	12/2013	1028.1	1028.1
80	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL)	6/2011	03/2018	03/2018	03/2018	1131.28	1131.28
81	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN	12/2011	08/2014	N.A.	08/2014	2422.66	2422.66

	JHARKHAND AND WEST BENGAL-PART-A						
82	Rajrappa RCE OCP	12/2009	03/2016	N.A.	03/2016	510.85	510.85
83	CHURCHA UG	6/2008	03/2014	03/2014	03/2014	462.35	462.35
84	Himmatnagar - Udaipur Gauge Canvession (NWR)	4/2008	03/2015	N.A.	03/2015	829.74	829.74
85	KANIHA OCP, MCL, (10.0 Mty)	12/2007	03/2013	03/2013	03/2013	457.77	457.77
86	MANIKPUR OC EXPANTION	11/2009	03/2014	03/2014	03/2014	321.42	321.5
87	BHUBANESWARI OCP, MCL (20.0 Mty)	12/2007	03/2017	03/2017	03/2017	490	490.1
88	GOPAL PRASAD OCP	2/2008	03/2015	03/2015	03/2015	395.87	395.87
89	TALABIRA OCP	3/2008	03/2016	03/2016	03/2016	447.72	447.72
90	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	03/2013	03/2013	03/2013	475.93	479.53
91	BINA EXTN. PROJ(6.0 Mtpa)	11/2006	03/2014	03/2014	03/2014	168.97	168.97
92	RKP OCP PHASE-I	3/2010	03/2015	N.A.	03/2015	209.78	209.78
93	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUB STATION AT KALA IN UT DNH	7/2011	07/2013	N.A.	07/2013	181.93	181.93
94	GAGAN PROJECT	9/2008	06/2013	N.A.	06/2013	626	626
95	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	6/2010	01/2014	N.A.	01/2014	202.94	202.94
96	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	3/2011	05/2013	N.A.	05/2013	861.79	756.65
97	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	7/2010	07/2015	N.A.	07/2015	1987	1987
98	NASHRI CHANANI	6/2010	06/2015	N.A.	06/2015	2159	2159
99	PATNA-MUZZAFFARPUR	8/2010	02/2013	N.A.	02/2013	671.3	671.3
100	4 LANNING OF AHMEDABAD TO GODHARA	12/2010	06/2013	N.A.	06/2013	1008.5	1008.5
101	4 LANNING OF GODHARA TO GUJARAT/MP BORDER	3/2011	08/2013	N.A.	08/2013	785.5	785.5
102	ROHTAK-BAWAL	5/2011	11/2013	N.A.	11/2013	650	650
103	GHAZIABAD-ALIGARH NH- 91	2/2011	08/2013	N.A.	08/2013	1141	1141
104	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00	6/2011	12/2013	N.A.	12/2013	535	535
105	SIX LANNING OF KRISHNAGIRI-	9/2011	12/2013	N.A.	12/2013	1250	1250

	WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46						
106	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	6/2011	06/2013	N.A.	06/2013	600	600
107	FARIDABAD EXTENSION	9/2011	09/2014	N.A.	09/2014	2494	2494
108	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART- A	10/2011	11/2013	N.A.	11/2013	558.26	558.26
109	Common System Associated with Coastal Energen Private Limited and Ind-Barath Power Madras Limited LT	9/2011	09/2014	N.A.	09/2014	1940.13	1940.13
110	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH	9/2011	12/2013	N.A.	12/2013	1366.34	1366.34
111	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED	8/2011	10/2013	N.A.	10/2013	425.51	425.51
112	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN	8/2011	12/2013	N.A.	12/2013	1391.97	1391.97
113	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT KALA IN UT DNH	7/2011	07/2013	N.A.	07/2013	181.93	181.93
114	SYTEM STRENGTHENING XIII OF SR GRID	10/2011	06/2014	N.A.	06/2014	487.49	487.49
115	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN	8/2011	12/2013	N.A.	12/2013	1391.97	1391.97
116	2 Laning of Muzaffarpur - Sonbarsa	5/2011	11/2013	N.A.	11/2013	511.54	511.54
117	Kandla - Mundra port	1/2011	07/2013	N.A.	07/2013	953.88	953.88
118	Two laning of Trichy - Karaikudi and Trychi Bypass	5/2010	05/2013	N.A.	05/2013	374	374
119	2 laning of Dindigul - Perigulam Theni- kumili	9/2011	08/2013	N.A.	08/2013	485	485
120	Tirupati - Tiruthani - Chennai	4/2011	10/2013	N.A.	10/2013	571	571

121	SAMAIKHALI - GANDHIDHAM	9/2010	03/2013	N.A.	03/2013	805.39	805.39
122	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNAM OF ANDHRA PRADESH(PGCIL)	8/2011	08/2014	N.A.	08/2014	1637.34	1637.34
123	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPs GENERATION PROJECTS IN CHATTISGARH	11/2011	07/2014	N.A.	07/2014	2127.51	2127.51
124	Muraidih UG Turn-key Project	2/2011	04/2014	N.A.	04/2014	339.88	339.88
125	Moonidih XV Seam UG	8/2011	04/2015	N.A.	04/2015	1230.27	1230.27
126	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED	12/2011	02/2014	N.A.	02/2014	552.44	552.44
127	Assam gas Cracker project	4/2006	12/2013	12/2013	12/2013	5460.61	8920
128	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV	12/2011	08/2014	N.A.	08/2014	297.33	297.33
129	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH-PART-E	12/2011	08/2014	N.A.	08/2014	1746.65	1746.65
130	Butadiene Extraction Unit(BDEU) at Panipat	11/2009	02/2013	N.A.	02/2013	341.5	341.5
131	Fluidized catalytic cracking unit(FCCU) revamp at Mathura Refinery	7/2010	01/2013	N.A.	01/2013	1000	1000
132	PARADIP-RAIPUR- SAMBALPUR- RANCHI PIPELINE	8/2009	09/2012	09/2012	09/2012	1793	1400
133	Construction of tanks and blending facility at Vadinar	2/2009	09/2012	09/2012	09/2012	267	267
134	COKE OVEN BATTERY NO. 4 PHASE-II	8/2007	10/2012	10/2012	10/2012	108	216.68
135	Integrated crude Oil handling facilities at Paradip(2nd SPM)	12/2009	06/2012	06/2012	06/2012	1492.33	1300
136	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY	4/2008	04/2013	04/2013	04/2013	825	1827
137	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW)	6/2011	12/2015	N.A.	12/2015	5907.11	5907.11
138	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP	1/2012	01/2015	N.A.	01/2015	1422.85	1422.85

	PROJECTS IN CHHATTISGARH						
139	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD	1/2012	01/2014	N.A.	01/2014	259.28	259.28
140	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	1/2011	01/2014	N.A.	01/2014	913.63	913.63
141	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT	1/2010	01/2013	01/2013	01/2013	1478.63	1478.63
142	JALAGAM VENGALA RAO OCP	7/2011	03/2015	N.A.	03/2015	447.06	447.06
143	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH	2/2012	02/2015	N.A.	02/2015	1310.85	1310.85
144	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP- PART C1	2/2012	08/2014	N.A.	08/2014	324.33	324.33
145	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP- PART B	2/2012	10/2014	N.A.	10/2014	1927.16	1927.16
146	JORBAT - BARAPANI	1/2011	01/2014	N.A.	01/2014	536	536
147	RCE OF INDARAM OCP(1.20 MTPA)	7/2011	03/2015	N.A.	03/2015	162.76	162.76
148	2-LANNING OF SHILONG BYPASS	2/2011	02/2014	N.A.	02/2014	226	226
149	VARANASI-AURANGABAD KM.786 TO KM.978.40	9/2011	03/2014	N.A.	03/2014	2848	2848
150	SIX LANNING OF NELLORE- CHILKALURIPET KM.1182.802 TO KM.1366.547	11/2011	05/2014	N.A.	05/2014	1535	1535
151	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	9/2011	03/2014	N.A.	03/2014	574	574
152	2-LANNING WITH PS MOTIHARI-RAXAUL	10/2011	04/2014	N.A.	04/2014	375.09	375.09
153	4-LANNING OF CHAPRA- HAJIPUR	1/2011	07/2013	N.A.	07/2013	575	575
154	2 LANNING OF MUZAFFARPUR - SONBARSA	5/2011	11/2013	N.A.	11/2013	511.54	511.54
155	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN	3/2012	09/2014	N.A.	09/2014	198.63	198.63

	REGION						
156	LINE BAYS AND REACTOR PROVISIONS AT POWERGRID SUBSTATIONS ASSOCIATED WITH SYSTEM STRENGTHENING COMMO	3/2012	03/2014	N.A.	03/2014	213.78	213.78
157	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH	3/2012	06/2015	N.A.	06/2015	9569.76	9569.76
158	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1	3/2012	06/2014	N.A.	06/2014	206.44	206.44
159	Integrated Development of B-127 fields	12/2011	03/2015	N.A.	03/2015	2059.63	2059.63
160	Heera and South Heera Redevelopment Ph-II	3/2012	05/2015	N.A.	05/2015	5608.4	5608.4
161	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS	12/2011	08/2014	N.A.	08/2014	901.77	901.77
162	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV	11/2011	11/2014	N.A.	11/2014	723.63	723.63
163	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B	2/2012	10/2014	N.A.	10/2014	3201.44	3201.44
164	BAROUD OC EXPANSION (RCE)- 3MTY	4/2012	03/2016	N.A.	03/2016	258.56	258.56
165	SRINAGAR TO BANIHAL	6/2011	06/2014	N.A.	06/2014	1100.7	1100.7
166	2laning with PS Gopalganj-Chappra	12/2011	05/2014	N.A.	05/2014	325	325
167	4-laning of Barhi-Hazaribagh	2/2012	02/2014	N.A.	02/2014	398	398
168	BHOPAL-SANCHI	10/2011	01/2013	N.A.	01/2013	209	209
169	PUNE-SHOLAPUR,Pkg-II	9/2011	01/2014	N.A.	01/2014	835	835
170	NIROLI-ROXY-RAJAMUNDA	7/2011	01/2014	N.A.	01/2014	586	586
171	BHUBANESWAR TO PURI	3/2011	08/2013	N.A.	08/2013	500.29	500.29
172	SAMBALPUR-BARGARH-CHHATTISGARH/ORISSA BORDER	11/2011	05/2014	N.A.	05/2014	909	909
173	PANIKHOLI-RIMOLI	3/2012	09/2014	N.A.	09/2014	1410	1410
174	JAIPUR-REENGUS	8/2010	02/2013	N.A.	02/2013	267.81	267.81
175	BEAWAR-PALI-PINDWARA	12/2011	06/2014	N.A.	06/2014	2388	2388

List of Delay Project w.r.t Original and Revised

(Apr,2012)

						Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
<u>Atomic Energy</u>									
1	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29 -	1,106.29	1,084.24	04/2011 04/2011	04/2012	12	12
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00 -	15,824.00	14,714.00	12/2008 -	03/2013	51	-
3	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00 -	11,459.00	1,679.00	12/2015 -	11/2016	11	-
4	RAJASTHAN ATOMIC POWER PROJECT -7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00 -	12,320.00	1,000.00	12/2016 -	03/2017	3	-
Total			38,056.29 -	40,709.29	18,477.24				
<u>Civil Aviation</u>									
5	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61 -	335.61	105.04	05/2012 -	08/2012	3	-
6	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	2,325.00	1,927.29	05/2011 03/2012	10/2012	17	7
7	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	309.46	182.97	01/2011 04/2013	04/2013	27	0
Total			2,587.58 -	2,970.07	2,215.30				
<u>Coal</u>									
8	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 3,027.59	3,027.59	2,400.12	06/2009 -	03/2013	45	-
9	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhand	04/2006	471.66 341.63	341.63	108.58	03/2011 03/2012	03/2013	24	12
10	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Uttar Pradesh	05/2006	789.88 741.62	741.62	331.78	03/2010 -	03/2013	36	-

List of Delay Project w.r.t Original and Revised

(Apr,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
11	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97 -	418.97	86.44	03/2012 -	03/2013	12	-
12	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19 -	181.19	36.96	03/2012 -	03/2013	12	-
13	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Orissa	01/2005	302.96 -	302.96	91.51	03/2010 -	03/2014	48	-
14	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,Chhatisgarh	07/2005	1,667.55 -	2,675.67	1,391.03	03/2010 -	03/2014	48	-
15	DIPKA EXPANSION OCP (SECL) (20-25 MTY) - [060100094]SECL,Chhatisgarh	07/2005	1,268.53 -	1,943.66	1,271.50	03/2010 -	03/2014	48	-
16	TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 4,909.54	4,909.54	2,801.35	03/2012 -	03/2014	24	-
17	RAJMAHAL OC EXP. - [N06000056]ECL,Multi State	02/2006	50.08 -	153.82	23.71	03/2011 -	03/2014	36	-
18	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Orissa	08/2008	207.28 -	207.28	99.57	03/2012 03/2012	03/2014	24	24
19	Churi Benti UG - [N06000083]CCL,Jharkhand	06/2007	163.51 -	163.51	34.06	03/2011 03/2012	03/2014	36	24
20	North Urimari OCP - [N06000084]CCL,Jharkhand	12/2007	179.87 -	179.87	62.60	03/2012 03/2012	03/2014	24	24
21	Tapin OCP - [N06000086]CCL,Jharkhand	08/2008	264.68 -	264.68	96.89	03/2012 03/2013	03/2014	24	12
22	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	09/2006	212.34 779.26	779.26	281.16	03/2013 09/2012	10/2014	19	25
23	KAKATIYA LAONGWALL - [N06000048]SCCL,Multi State	12/2008	453.63 -	453.63	71.37	12/2012 -	01/2015	25	-
24	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04 535.10	535.10	161.77	03/2012 03/2015	03/2015	36	0
25	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18 -	287.17	-	03/2011 -	03/2015	48	-

List of Delay Project w.r.t Original and Revised

(Apr,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
26	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40 -	259.40	1.20	03/2012 -	03/2015	36	-
27	BALRAM OCP EXTENSION,MCL (8.00 Mty) - [N06000044]MCL,Orissa	12/2007	172.08 -	172.08	101.78	03/2010 -	03/2015	60	-
28	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77 -	339.77	0.82	03/2014 -	03/2015	12	-
29	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]NCL,Madhya pradesh	05/2006	1,352.04 1,143.54	1,143.54	317.40	03/2014 03/2016	03/2016	24	0
30	MAGADH OC (CCL) - [N06000015]CCL,Jharkhand	07/2006	469.78 706.40	706.40	18.16	07/2012 03/2014	03/2016	44	24
Total			17,193.74 -	20,188.34	9,789.76				
<u>Fertilisers</u>									
31	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00 -	325.00	174.37	07/2011 -	04/2012	9	-
32	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00 -	438.00	218.37	07/2011 -	07/2012	12	-
Total			763.00 -	763.00	392.74				
<u>Steel</u>									
33	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]SAIL,Chhatisgarh	07/2007	232.93 -	232.93	191.33	05/2011 -	05/2012	12	-
34	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00 -	350.00	241.50	08/2010 08/2010	06/2012	22	22
35	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00 -	343.58	246.84	02/2011 02/2011	07/2012	17	17
36	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00 12,291.00	12,291.00	9,513.66	10/2009 10/2012	10/2012	36	0

List of Delay Project w.r.t Original and Revised

(Apr,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
37	Bailadila Iron Ore Deposit-IIB(NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89 607.17	607.17	327.39	12/2011 03/2012	10/2012	10	7
38	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00 -	450.00	192.17	05/2012 05/2012	02/2013	9	9
39	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,West Bengal	06/2009	2,875.00 -	2,875.00	750.85	12/2012 -	03/2013	3	-
Total			13,065.82 -	17,149.68	11,463.74				
<u>Petroleum</u>									
40	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra	05/2008	333.40 837.54	656.51	554.93	05/2010 04/2012	05/2012	24	1
41	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32 -	330.47	202.86	03/2012 03/2012	06/2012	3	3
42	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	5,314.79	05/2010 05/2012	07/2012	26	2
43	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	825.10	07/2010 05/2012	07/2012	24	2
44	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11 -	370.11	211.24	04/2011 -	07/2012	15	-
45	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- - [N16000070]GAIL,Multi State	07/2009	238.68 252.37	204.00	169.73	01/2012 -	07/2012	6	-
46	KOCHI-KOOTANAD BANGALORE-MANGALORE PIPELINE PROJECT - [N16000071]GAIL,Multi State	06/2009	348.00 -	261.00	193.21	03/2012 08/2012	08/2012	5	0
47	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State	06/2009	4,543.43 4,508.38	2,300.00	1,706.48	03/2012 08/2012	08/2012	5	0
48	COMPRESSOR STATIONS (KAILARAS AND CHAINSA) - [N16000054]GAIL,Multi State	11/2007	1,167.00 -	798.00	707.41	04/2011 12/2011	09/2012	17	9

List of Delay Project w.r.t Original and Revised

(Apr,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	6
49	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	1,156.52	09/2011 03/2012	09/2012	12	
50	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	755.76	549.84	03/2011 05/2011	10/2012	19	17
51	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 12,160.26	12,160.26	8,582.11	01/2012 -	10/2012	9	-
52	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	12/2012	80	6
53	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	287.21	09/2011 -	12/2012	15	-
54	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 -	2,163.64	926.83	06/2012 -	12/2012	6	-
55	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	288.04	165.42	08/2012 -	12/2012	4	-
56	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	302.26	19.83	09/2012 -	12/2012	3	-
57	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	977.00	282.27	12/2011 -	01/2013	13	-
58	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	265.66	03/2006 03/2013	03/2013	84	0
59	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	6,939.45	05/2010 03/2013	03/2013	34	0
60	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92 -	460.70	195.06	07/2012 07/2012	03/2013	8	8
61	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	04/2013	52	0
62	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,273.53	09/2010 03/2012	04/2013	31	13

List of Delay Project w.r.t Original and Revised

(Apr,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
63	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 -	3,241.03	199.90	03/2013 -	04/2013	1	-
64	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	36.64	03/2013 -	04/2013	1	-
65	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	820.00	-	06/2012 -	04/2013	10	-
66	KOCHI KOOTTANAD BANGLORE MANGLORE PIPELINE PH-II - [N16000129]GAIL,Multi State	06/2009	2,915.00 -	2,915.00	885.82	12/2012 12/2012	04/2013	4	4
67	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	479.11	03/2010 03/2012	05/2013	38	14
68	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	7.33	11/2012 -	05/2013	6	-
69	PARADIP REFINERY PROJECT - [N16000058]IOCL,Orissa	02/2009	29,777.00 -	30,426.00	15,205.00	11/2012 06/2013	06/2013	7	0
70	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	6,855.93	3,427.22	09/2012 -	09/2013	12	-
71	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	723.64	-	03/2013 -	11/2013	8	-
72	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	3,499.88	08/2010 03/2012	12/2013	40	21
73	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	269.10	-	08/2013 -	01/2014	5	-
74	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	594.10	03/2007 03/2014	03/2014	84	0
75	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	2,378.86	589.72	03/2013 -	03/2014	12	-
76	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	281.07	3.41	10/2010 -	12/2014	50	-

List of Delay Project w.r.t Original and Revised

(Apr,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
77	Development of C-26 Cluster Fields - [N16000133]ONGC,Maharashtra	03/2012	2,592.17 -	2,592.17	-	05/2014 -	03/2015	10	-
78	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	7,596.18	2.20	01/2013 -	07/2015	30	-
79	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,481.56	03/2007 03/2017	03/2017	120	0
Total			109,624.68	119,448.90	61,646.28				
<u>Power</u>									
80	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL, Uttar Pradesh	07/2006	1,657.00 2,978.86	2,978.86	321.09	07/2010 02/2016	02/2016	67	0
81	SIPAT STPP STAGE - I (NTPC) - [180100229]NTPC,Chhatisgarh	12/2003	8,323.39 -	8,323.39	8,194.00	12/2009 12/2011	05/2012	29	5
82	CHAMERA,STAGE-III (NHPC) - [180100241]NHPC,Himachal Pr.	08/2005	1,405.63 -	2,084.00	1,815.30	08/2010 08/2011	06/2012	22	10
83	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) - [180100260]PGCIL,Bihar	12/2005	3,779.46 -	3,779.46	3,681.30	09/2009 -	06/2012	33	-
84	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]PGCIL,Multi State	02/2009	409.50 -	409.50	103.30	02/2012 02/2012	06/2012	4	4
85	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69 -	317.69	180.40	11/2011 11/2011	06/2012	7	7
86	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10 -	196.10	132.50	07/2011 -	06/2012	11	-
87	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92 -	1,628.39	1,476.77	03/2007 -	09/2012	66	-

List of Delay Project w.r.t Original and Revised

(Apr,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
88	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37 -	297.91	326.43	07/2011 -	09/2012	14	-
89	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J and K	08/2006	621.26 -	621.28	733.22	02/2011 -	10/2012	20	-
90	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32 -	1,347.32	1,031.20	02/2012 -	10/2012	8	-
91	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96 -	975.96	829.70	10/2009 -	12/2012	38	-
92	LOHARINAG-PAL HEP(4X150MW) - [N18000005]NTPC,Uttaranchal	06/2006	2,895.10 -	2,895.10	690.00	11/2011 -	12/2012	13	-
93	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23 -	5,221.23	3,123.60	07/2010 -	12/2012	29	-
94	SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95 -	2,360.95	1,916.40	08/2012 -	12/2012	4	-
95	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36 -	1,736.36	929.20	06/2012 -	12/2012	6	-
96	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	1,075.12	567.70	05/2012 -	12/2012	7	-
97	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83 -	1,216.83	704.20	08/2012 -	12/2012	4	-
98	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.56 -	2,716.00	1,788.59	10/2010 12/2011	01/2013	27	13

List of Delay Project w.r.t Original and Revised

(Apr,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
99	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J and K	08/2006	611.01 -	936.00	729.82	08/2010 09/2011	01/2013	29	16
100	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J and K	08/2005	1,729.29 -	1,794.00	1,715.58	11/2009 11/2011	02/2013	39	15
101	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24 -	557.24	549.00	01/2010 -	02/2013	37	-
102	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28 -	6,010.89	4,047.00	08/2012 -	03/2013	7	-
103	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	149.00	11/2011 -	03/2013	16	-
104	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	5,161.60	08/2012 -	03/2013	7	-
105	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya Pradesh	01/2009	5,915.00 -	5,915.00	3,402.00	10/2012 -	03/2013	5	-
106	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	3,163.00	10/2012 -	03/2013	5	-
107	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	4,672.99	1,182.10	11/2012 -	03/2013	4	-
108	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	731.60	12/2012 -	03/2013	3	-
109	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32 -	160.32	38.90	10/2012 -	03/2013	5	-
110	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	1,501.75	1,112.46	09/2009 -	06/2013	45	-

List of Delay Project w.r.t Original and Revised

(Apr,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
111	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	520.48	11/2011 -	06/2013	19	-
112	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	324.10	11/2011 -	06/2013	19	-
113	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	226.20	02/2012 -	06/2013	16	-
114	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	383.60	11/2012 -	06/2013	7	-
115	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	386.00	04/2013 -	06/2013	2	-
116	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pr.	01/2007	2,047.03 -	2,047.03	1,658.86	01/2012 -	09/2013	20	-
117	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	4,824.12	2,687.70	10/2012 -	09/2013	11	-
118	EASTERN REGION TRANSMISSION SYSTEM- III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	1,272.80	291.40	11/2012 -	09/2013	10	-
119	KOLDAM HEP (NTPC) - [180100211]NTPC, Himachal Pr.	10/2002	4,527.15 -	4,527.15	4,260.00	04/2009 03/2014	03/2014	59	0
120	BARH STPP STAGE -II - [N18000047]NTPC, Bihar	02/2008	7,341.04 -	7,341.04	4,218.00	08/2013 -	06/2014	10	-
121	PARBATI HEP (NHPC) II - [180100210]NHPC, Himachal Pr.	09/2002	3,919.59 -	5,524.00	3,405.19	09/2009 07/2014	07/2014	58	0
122	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO, Arunachal Pr.	12/2008	573.99 -	573.99	314.41	08/2012 08/2013	09/2014	25	13

List of Delay Project w.r.t Original and Revised

(Apr,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
123	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	4,502.50	08/2013 -	09/2014	13	-
124	TUIRIAL HE PROJECT(NEEPCO) - [180100165]NEEPCO,Mizoram	07/1998	368.72 913.63	913.63	307.53	07/2006 01/2014	02/2015	103	13
125	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttaranchal	11/2006	2,978.48 -	2,978.48	1,457.00	03/2013 -	09/2015	30	-
126	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pr.	09/2003	6,285.33 -	10,667.00	5,653.06	09/2010 08/2014	12/2015	63	16
127	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97 -	8,693.00	6,961.00	12/2009 12/2014	03/2016	75	15
128	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttaranchal	08/2008	2,491.58 2,491.58	3,422.44	302.52	07/2014 -	05/2016	22	-
129	KISHANGANGA HEP - [N18000031]NHPC,J and K	07/2007	2,238.67 3,642.04	3,642.00	1,411.76	01/2016 01/2016	11/2016	10	10
130	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pr.	12/2004	2,496.90 -	2,496.90	1,829.23	05/2013 06/2016	03/2017	46	9
Total			137,982.73	151,501.32	91,627.50				
<u>Railways</u>									
131	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 261.70	261.70	39.12	02/2006 -	12/2012	82	-
132	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]ECR,Bihar	04/1997	100.00 483.62	484.03	455.07	03/2012 03/2012	06/2012	3	3
133	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR,Gujarat	04/2006	196.97 -	196.97	213.97	03/2011 -	06/2012	15	-
134	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 -	456.45	281.69	06/2004 -	12/2012	102	-
135	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	500.00	559.46	03/2012 03/2012	12/2012	9	9

List of Delay Project w.r.t Original and Revised

(Apr,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
136	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 -	341.41	263.32	03/2012 03/2012	12/2012	9	9
137	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 -	1,115.63	693.29	03/2009 12/2012	12/2012	45	0
138	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 1,389.98	1,389.98	1,230.99	10/2007 12/2012	12/2012	62	0
139	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	687.20	-	03/2010 -	12/2012	33	-
140	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	634.13	550.42	03/1995 -	03/2013	216	-
141	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 -	603.04	59.64	03/2012 -	03/2013	12	-
142	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	243.40	-	02/2009 02/2009	04/2013	50	50
143	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	225.00	-	03/2009 03/2009	04/2013	49	49
144	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 -	207.52	126.13	12/2012 -	05/2013	5	-
145	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	611.03	89.65	12/2011 11/2013	11/2013	23	0
146	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 -	4,255.37	3,055.16	03/2009 -	12/2013	57	-
147	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	499.16	160.99	03/2007 03/2007	03/2014	84	84
148	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 -	1,655.80	1,086.71	12/2008 -	03/2014	63	-
149	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 -	223.01	104.88	12/2012 -	03/2014	15	-
150	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00 -	819.40	142.97	03/2010 06/2014	06/2014	51	0

List of Delay Project w.r.t Original and Revised

(Apr,2012)

						Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
151	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,041.79	728.94	12/2010 12/2010	03/2015	51	51
152	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	5,300.00	698.48	03/2014 03/2015	03/2015	12	0
153	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	3,230.01	2,387.21	04/2008 03/2014	12/2015	92	21
154	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,028.05	1,412.74	425.46	03/2005 12/2008	12/2015	129	84
155	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 529.23	529.23	227.13	02/2010 -	12/2015	70	-
156	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 -	3,056.85	738.60	03/2011 03/2014	03/2016	60	24
157	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,069.60	24.59	03/2014 03/2016	03/2016	24	0
158	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	1,086.41	404.60	06/2005 07/2011	06/2016	132	59
159	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	21.85	03/2016 -	06/2016	3	-
160	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J and K	03/1995	2,500.00 8,000.00	20,000.00	7,933.78	03/2001 -	12/2017	201	-
Total			22,991.83	55,534.58	22,704.10				
<u>Road Transport & Highways</u>									
161	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI,West Bengal	04/2000	273.00 -	522.00	475.55	03/2005 -	05/2012	86	-
162	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI,J and K	12/2003	193.09 -	166.30	184.94	03/2008 -	05/2012	50	-

List of Delay Project w.r.t Original and Revised

(Apr,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
163	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J and K	12/2003	166.27 -	193.10	161.44	03/2008 -	05/2012	50	-
164	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI,Uttar Pradesh	12/2003	227.00 -	227.00	383.29	12/2008 -	05/2012	41	-
165	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI,Madhya pradesh	12/2003	225.00 -	225.00	261.98	10/2008 -	05/2012	43	-
166	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI,Uttar Pradesh	12/2003	151.30 -	151.30	180.94	10/2008 -	05/2012	43	-
167	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00 -	245.00	491.21	03/2008 -	05/2012	50	-
168	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00 -	941.00	1,901.00	01/2011 -	05/2012	16	-
169	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00 -	557.00	930.92	02/2010 -	05/2012	27	-
170	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47 -	154.57	195.52	09/2007 -	06/2012	57	-
171	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	196.65	171.29	08/2004 07/2010	06/2012	94	23
172	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	207.56	180.97	08/2004 -	06/2012	94	-
173	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49 -	367.49	453.68	03/2005 -	06/2012	87	-
174	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI,Uttar Pradesh	12/2003	275.00 -	275.00	304.24	09/2007 -	06/2012	57	-
175	HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	220.00	272.96	09/2007 -	06/2012	57	-

List of Delay Project w.r.t Original and Revised

(Apr,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
176	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00 -	201.66	112.02	09/2008 -	06/2012	45	-
177	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00 -	240.00	285.56	10/2008 -	06/2012	44	-
178	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68 -	340.68	370.49	03/2008 -	06/2012	51	-
179	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00 -	190.00	254.19	01/2009 -	06/2012	41	-
180	DAKOBA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00 -	225.00	267.44	06/2008 -	06/2012	48	-
181	BIJUNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	195.00	196.85	06/2008 -	06/2012	48	-
182	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar	12/2003	340.00 -	340.00	498.63	09/2008 -	06/2012	45	-
183	NALBARI TO BIJUNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00 -	200.00	273.20	06/2008 -	06/2012	48	-
184	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50 363.00	363.00	248.66	06/2011 06/2011	06/2012	12	12
185	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	264.72	272.48	06/2008 -	06/2012	48	-
186	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82 -	221.82	278.86	11/2008 -	06/2012	43	-
187	NALBARI TO BIJUNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00 -	225.00	226.70	06/2008 -	06/2012	48	-
188	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00 -	160.00	164.32	05/2008 -	06/2012	49	-
189	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	200.00	209.81	06/2008 -	06/2012	48	-
190	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00 -	168.00	457.30	12/2008 -	06/2012	42	-

List of Delay Project w.r.t Original and Revised

(Apr,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
191	GANJAM- ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27 -	263.27	265.81	02/2004 -	06/2012	100	-
192	END OF DURG BYPASS- CHHATISGARH/MAHARAS HTRA BORDER - [N24000118]NHAI, Chhatisga rh	01/2008	464.00 -	464.00	534.79	01/2011 -	06/2012	17	-
193	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70 -	1,673.70	2,406.10	10/2011 -	06/2012	8	-
194	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75 -	1,693.75	2,638.80	08/2011 -	06/2012	10	-
195	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56 -	390.56	631.65	02/2012 -	06/2012	4	-
196	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00 -	241.53	113.73	04/2004 -	07/2012	99	-
197	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70 -	228.70	182.07	02/2004 -	07/2012	101	-
198	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH- 1A - [240106237]NHAI,Punjab	12/2003	284.00 -	359.00	191.60	05/2008 -	08/2012	51	-
199	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	230.00	224.58	06/2005 -	09/2012	87	-
200	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	250.39	279.31	10/2008 -	09/2012	47	-
201	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA - [240106305]NHAI,Madhya pradesh	12/2003	229.91 -	229.91	247.95	10/2008 -	09/2012	47	-
202	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI, Madhya pradesh	12/2003	407.60 -	407.60	185.52	06/2010 -	10/2012	28	-
203	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI, Madhya pradesh	12/2003	263.17 -	263.17	233.77	09/2009 -	10/2012	37	-

List of Delay Project w.r.t Original and Revised

(Apr,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
204	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI, Maharashtra	04/2010	1,170.52 -	1,170.52	4.41	06/2011 -	10/2012	16	-
205	THANJAUR-TRICHY, NH-67(NHAI) - [N24000056]NHAI, Tamil Nadu	03/2005	280.00 -	280.00	581.49	06/2009 -	11/2012	41	-
206	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI, Bihar	12/2003	300.00 -	300.00	170.23	10/2008 -	12/2012	50	-
207	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI, Assam	12/2003	237.80 -	237.80	238.58	06/2008 -	12/2012	54	-
208	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI, Bihar	12/2003	332.94 -	332.94	357.43	09/2008 -	12/2012	51	-
209	SAGAR - RAJMARG CHORAHA, KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI, Madhya pradesh	12/2003	203.43 -	203.43	229.13	10/2008 -	12/2012	50	-
210	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, Madhya pradesh	12/2003	251.03 -	251.03	297.84	10/2008 -	12/2012	50	-
211	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, West Bengal	12/2003	225.00 -	225.00	180.10	07/2008 -	12/2012	53	-
212	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, Assam	12/2003	175.96 -	175.96	140.59	04/2008 -	12/2012	56	-
213	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, Assam	12/2003	198.16 -	198.16	202.60	04/2008 -	12/2012	56	-
214	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00 -	208.00	255.94	04/2008 -	12/2012	56	-
215	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, Assam	12/2003	217.61 -	217.61	188.81	04/2010 -	12/2012	32	-
216	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI, Madhya pradesh	12/2003	300.93 -	300.93	302.72	10/2009 -	12/2012	38	-
217	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, Multi State	12/2003	604.00 -	604.00	494.29	12/2009 -	12/2012	36	-

List of Delay Project w.r.t Original and Revised

(Apr,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
218	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06 -	355.06	436.86	09/2009 -	12/2012	39	-
219	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45 -	232.45	251.79	09/2010 -	12/2012	27	-
220	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00 -	486.00	577.73	05/2010 -	12/2012	31	-
221	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	280.00	259.81	02/2009 -	03/2013	49	-
222	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	200.00	96.26	04/2009 -	03/2013	47	-
223	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00 -	516.00	719.55	07/2010 -	03/2013	32	-
224	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16 -	465.50	151.69	09/2007 -	06/2013	69	-
225	Chilkaluript-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30 -	572.30	647.98	10/2011 -	06/2013	20	-
226	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00 -	2,288.00	3,454.50	11/2011 -	06/2013	19	-
227	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00 -	705.00	935.59	11/2012 -	06/2013	7	-
228	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81 -	385.13	48.94	04/2009 -	07/2013	51	-
229	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04 -	280.13	85.39	11/2008 -	07/2013	56	-
230	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00 -	617.00	154.52	08/2012 -	10/2013	14	-
231	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	281.31	179.23	02/2010 -	12/2013	46	-

List of Delay Project w.r.t Original and Revised

(Apr,2012)

						Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
232	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	167.64	6.00	11/2008 -	01/2014	62	-
233	INDORE-DEWAS(NH-3) - [N24000159]NHAI, Madhya pradesh	11/2010	325.00 -	325.00	316.92	05/2013 -	02/2014	9	-
234	Chennai-Tada(Six lane) - [N24000129]NHAI, Tamil Nadu	04/2009	353.37 -	353.37	231.86	10/2011 -	03/2014	29	-
235	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, Bihar	05/2011	351.54 -	351.54	163.93	05/2013 -	03/2014	10	-
236	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI, Assam	12/2003	212.00 -	386.10	21.81	09/2007 -	04/2014	79	-
237	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, Assam	12/2003	196.00 -	363.74	34.23	07/2009 -	04/2014	57	-
238	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, Bihar	05/2011	664.00 -	664.00	15.15	02/2014 -	04/2014	2	-
239	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, J and K	07/2010	1,813.76 -	1,813.76	-	07/2013 -	06/2014	11	-
240	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI, Karnataka	03/2011	359.00 -	359.00	32.41	09/2013 -	07/2014	10	-
Total			29,705.51 -	32,032.84	31,268.43				
<u>Shipping & Ports</u>									
241	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Mahara shtra	10/2007	359.44 -	359.44	358.78	04/2011 06/2011	06/2012	14	12
242	Acquisition of two nos. of 120 B.P BY 079& 080 - [N25000042]SHIPP.,Mahara shtra	04/2009	290.85 -	305.00	86.46	06/2011 06/2012	06/2012	12	0
243	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Mahara shtra	04/2009	277.03 280.00	277.03	81.40	12/2011 08/2012	08/2012	8	0
244	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST, Kerala	03/2009	3,500.00 4,150.00	4,150.00	3,240.30	01/2012 09/2012	09/2012	8	0

List of Delay Project w.r.t Original and Revised

(Apr,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
245	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST, Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	29	-
246	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU, Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	743.63	12/2010 -	12/2012	24	-
247	CONSTRUCTION OF Berthing and Allied Facilities off - [N25000037]PORT TRUST, Gujarat	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012	22	-
248	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST, Gujarat	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	24	-
249	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST, Tamil Nadu	10/2002	150.00 600.00	600.00	67.00	03/2006 -	12/2013	93	-
Total			7,833.42 -	9,411.07	4,797.50				
Telecommunications									
250	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL, Multi State	11/2003	250.00 -	250.00	80.47	12/2005 03/2008	05/2012	77	50
251	NIB Project Capacity Expansion - [N260000098]BSNL, Multi State	06/2007	175.52 -	175.52	60.84	12/2008 -	05/2012	41	-
252	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N260000041]BSNL, Punjab	02/2008	373.94 -	373.94	227.29	12/2008 -	06/2012	42	-
253	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N260000058]BSNL, Uttaranchal	01/2009	149.15 158.72	158.72	76.55	06/2009 -	06/2012	36	-
254	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N260000062]BSNL, Assam	06/2007	336.81 -	336.81	157.98	01/2009 -	06/2012	41	-
255	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N260000088]BSNL, Jharkhand	03/2008	328.13 -	328.12	164.58	03/2009 -	06/2012	39	-

List of Delay Project w.r.t Original and Revised

(Apr,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
256	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	384.00	21.93	10/2010 03/2012	07/2012	21	4
	Total		1,997.55 -	2,007.11	789.64				
<u>Urban Development</u>									
257	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00 -	11,609.00	2,267.57	12/2011 -	12/2013	24	-
	Total		6,395.00 -	11,609.00	2,267.57				
<u>Water Resources</u>									
258	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012	60	-
	Total		542.90 -	1,187.00	35.49				
Grand Total			388,740.05	464,512.20	257,475.29				



Date of Commissioning

Steel

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
15	1.2 MTPA PELLET PLANT DONIMALAI - [N12000072]NMDC,Karnataka	04/2011	572.00 -	04/2013 -	04/2013	0/0
16	7.0 MTPA KUMARASWAMY IRON ORE MINE - [N12000073]NMDC,Karnataka	02/2011	898.55 -	05/2013 -	05/2013	0/0
	Total		1,470.55 -			0/0
<u>Petroleum</u>						
17	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 -	09/2011 -	03/2012	0/0
18	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 299.00	02/2011 08/2011	08/2011	0/0
19	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra	05/2008	333.40 837.54	05/2010 04/2012	05/2012	0/0
20	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	05/2010 05/2012	07/2012	0/0
21	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	07/2010 05/2012	07/2012	0/0
22	ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11 -	04/2011 -	07/2012	0/0
23	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	07/2012 -	07/2012	0/0
24	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	09/2011 03/2012	09/2012	0/0
25	CONSTRUCTION OF TANKS AND BLENDING FACILITY AT VAD - [N16000115]IOCL,Gujarat	02/2009	267.00 -	09/2012 09/2012	09/2012	0/0
26	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	03/2011 05/2011	10/2012	0/0
27	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 12,160.26	01/2012 -	10/2012	0/0
28	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	04/2006 06/2012	12/2012	0/0
29	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	09/2011 -	12/2012	0/0
30	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 -	06/2012 -	12/2012	0/0
31	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	08/2012 -	12/2012	0/0
32	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	09/2012 -	12/2012	0/0
33	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	12/2011 -	01/2013	0/0
34	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	05/2010 03/2013	03/2013	0/0
35	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	12/2008 04/2013	04/2013	0/0
36	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	09/2010 03/2012	04/2013	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
37	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 -	03/2013 -	04/2013	0/0
38	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	03/2013 -	04/2013	0/0
39	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	06/2012 -	04/2013	0/0
40	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	03/2010 03/2012	05/2013	0/0
41	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	11/2012 -	05/2013	0/0
42	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79 -	05/2013 -	05/2013	0/0
43	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	09/2012 -	09/2013	0/0
44	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	03/2013 -	11/2013	0/0
45	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	08/2010 03/2012	12/2013	0/0
46	Wax Project - [N16000101]NRL,Assam	06/2010	576.60 -	12/2013 12/2013	12/2013	0/0
47	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	01/2014 -	01/2014	0/0
48	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	08/2013 -	01/2014	0/0
49	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER - [N16000127]ONGC,Assam	06/2010	202.94 -	01/2014 -	01/2014	0/0
50	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00 -	02/2014 -	02/2014	0/0
51	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	03/2013 -	03/2014	0/0
52	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	10/2010 -	12/2014	0/0
53	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10 -	12/2014 -	12/2014	0/0
54	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63 -	12/2014 -	12/2014	0/0
55	Integrated Development of B-127 fields - [N16000131]ONGC,Maharashtra	12/2011	2,059.63 -	03/2015 -	03/2015	0/0
56	Development of C-26 Cluster Fields - [N16000133]ONGC,Maharashtra	03/2012	2,592.17 -	05/2014 -	03/2015	0/0
57	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00 -	04/2015 -	04/2015	0/0
58	Heera and South Heera Redevelopment Ph-II - [N16000132]ONGC,Maharashtra	03/2012	5,608.40 -	05/2015 -	05/2015	0/0
59	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	01/2013 -	07/2015	0/0
60	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	- -	-	0/0
61	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON - [N16000009]BRPL,Assam	06/2006	1,431.91 1,646.39	09/2009 -	-	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	Total		102,750.02			0/0
			-			
	<u>Power</u>					
62	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61	04/2012	04/2012	0/0
			-	-		
63	MAUDA TRANSMISSION SYSTEM - [N18000084]PGCIL,Maharashtra	02/2010	469.38	10/2012	05/2012	0/0
			-	-		
64	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]PGCIL,Multi State	02/2009	409.50	02/2012	06/2012	0/0
			-	02/2012		
65	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69	11/2011	06/2012	0/0
			-	11/2011		
66	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10	07/2011	06/2012	0/0
			-	-		
67	IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS - [N18000082]PGCIL,Bihar	02/2010	215.86	06/2012	06/2012	0/0
			-	-		
68	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34	06/2012	06/2012	0/0
			-	-		
69	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37	07/2011	09/2012	0/0
			-	-		
70	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32	02/2012	10/2012	0/0
			-	-		
71	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88	12/2012	12/2012	0/0
			-	-		
72	SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95	08/2012	12/2012	0/0
			-	-		
73	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36	06/2012	12/2012	0/0
			-	-		
74	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12	05/2012	12/2012	0/0
			-	-		
75	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83	08/2012	12/2012	0/0
			-	-		
76	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68	01/2013	01/2013	0/0
			-	-		
77	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03	01/2013	01/2013	0/0
			-	-		
78	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19	11/2011	03/2013	0/0
			-	-		
79	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33	08/2012	03/2013	0/0
			-	-		
80	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99	11/2012	03/2013	0/0
			-	-		

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
81	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	12/2012 -	03/2013	0/0
82	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Orissa	09/2010	2,074.86 -	03/2013 -	03/2013	0/0
83	INTERCONNECTION BETWEEN ELECTTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32 -	10/2012 -	03/2013	0/0
84	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36 -	04/2013 -	04/2013	0/0
85	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	09/2009 -	06/2013	0/0
86	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	11/2011 -	06/2013	0/0
87	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	11/2011 -	06/2013	0/0
88	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	02/2012 -	06/2013	0/0
89	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	11/2012 -	06/2013	0/0
90	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	04/2013 -	06/2013	0/0
91	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64 -	07/2013 -	07/2013	0/0
92	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93 -	07/2013 -	07/2013	0/0
93	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000108]PGCIL,Madhya pradesh	07/2011	181.93 -	07/2013 -	07/2013	0/0
94	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM - [N18000090]PGCIL,Andhra Pradesh	12/2010	779.21 -	08/2013 -	08/2013	0/0
95	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII - [N18000091]PGCIL,Multi State	12/2010	209.78 -	08/2013 -	08/2013	0/0
96	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52 -	08/2013 -	08/2013	0/0
97	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pr.	01/2007	2,047.03 -	01/2012 -	09/2013	0/0
98	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	10/2012 -	09/2013	0/0
99	EASTERN REGION TRANSMISSION SYSTEM- III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	11/2012 -	09/2013	0/0
100	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,Madhya pradesh	08/2011	425.51 -	10/2013 -	10/2013	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
101	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL,Multi State	03/2011	1,585.12 -	11/2013 -	11/2013	0/0
102	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARK - [N18000104]PGCIL,Jharkhandd	10/2011	558.26 -	11/2013 -	11/2013	0/0
103	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Orissa	12/2010	2,743.19 -	12/2013 -	12/2013	0/0
104	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CH - [N18000105]PGCIL,Multi State	09/2011	1,366.34 -	12/2013 -	12/2013	0/0
105	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000107]PGCIL,Chhatisgarh	08/2011	1,391.97 -	12/2013 -	12/2013	0/0
106	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH - [N18000110]PGCIL,Multi State	08/2011	1,391.97 -	12/2013 -	12/2013	0/0
107	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000118]PGCIL,Gujarat	01/2012	259.28 -	01/2014 -	01/2014	0/0
108	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,Mizoram	01/2011	913.63 -	01/2014 -	01/2014	0/0
109	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT - [N18000114]PGCIL,Gujarat	12/2011	552.44 -	02/2014 -	02/2014	0/0
110	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL,Multi State	03/2011	2,569.25 -	03/2014 -	03/2014	0/0
111	LINE BAYS AND REACTOR PROVISIONS AT POWERGRID SUBSTATIONS AS - [N18000124]PGCIL,Madhya pradesh	03/2012	213.78 -	03/2014 -	03/2014	0/0
112	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA - [N18000101]PGCIL,Chhatisgarh	05/2011	1,961.87 -	05/2014 -	05/2014	0/0
113	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,Multi State	10/2011	487.49 -	06/2014 -	06/2014	0/0
114	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA - [N18000126]PGCIL,Andhra Pradesh	03/2012	206.44 -	06/2014 -	06/2014	0/0
115	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR - [N18000112]PGCIL,Chhatisgarh	11/2011	2,127.51 -	07/2014 -	07/2014	0/0
116	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNA - [N18000111]PGCIL,Andhra Pradesh	08/2011	1,637.34 -	08/2014 -	08/2014	0/0
117	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND W - [N18000113]PGCIL,Multi State	12/2011	2,422.66 -	08/2014 -	08/2014	0/0
118	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,Multi State	12/2011	297.33 -	08/2014 -	08/2014	0/0
119	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR - [N18000116]PGCIL,Chhatisgarh	12/2011	1,746.65 -	08/2014 -	08/2014	0/0
120	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000121]PGCIL,Andhra Pradesh	02/2012	324.33 -	08/2014 -	08/2014	0/0
121	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,Bihar	12/2011	901.77 -	08/2014 -	08/2014	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
122	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	08/2013 -	09/2014	0/0
123	Common System Associated with Coastal Energen Priv - [N18000103]PGCIL,Tamil Nadu	09/2011	1,940.13 -	09/2014 -	09/2014	0/0
124	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123]PGCIL,Multi State	03/2012	198.63 -	09/2014 -	09/2014	0/0
125	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000122]PGCIL,Andhra Pradesh	02/2012	1,927.16 -	10/2014 -	10/2014	0/0
126	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART- - [N18000129]PGCIL,Multi State	02/2012	3,201.44 -	10/2014 -	10/2014	0/0
127	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,Multi State	11/2011	723.63 -	11/2014 -	11/2014	0/0
128	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR - [N18000077]PGCIL,West Bengal	04/2010	4,404.57 -	01/2015 -	01/2015	0/0
129	SYSTEM STRENGTHENING IN RAIPUR- WARDHA CORRIDOR FOR IPP PROJEC - [N18000117]PGCIL,Chhatisgarh	01/2012	1,422.85 -	01/2015 -	01/2015	0/0
130	SYSTEM STRENGTHENING IN WARDHA- AURANGABAD CORRIDOR FOR IPP P - [N18000120]PGCIL,Maharashtra	02/2012	1,310.85 -	02/2015 -	02/2015	0/0
131	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,Chhatisgarh	03/2012	9,569.76 -	06/2015 -	06/2015	0/0
132	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	09/2010 -	-	0/0
	Total		113,603.02 -			0/0
Railways						
133	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	03/1998 -	03/1998	0/0
134	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	04/2003 03/2010	03/2010	0/0
135	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	06/2008	0/0
136	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhandd	03/1997	186.92 261.70	02/2006 -	12/2012	0/0
137	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 1,099.20	07/2005 -	07/2005	0/0
138	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94 604.04	03/1998 08/2005	08/2005	0/0
139	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30	06/2007 -	06/2007	0/0
140	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	07/2008 -	07/2008	0/0
141	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	- 05/2009	05/2009	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
142	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP, West Bengal	03/2000	907.69 3,176.10	12/2006 08/2010	08/2010	0/0
143	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP, Maharashtra	03/1996	401.81 495.44	03/2004 12/2010	12/2010	0/0
144	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL, Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	12/2010	0/0
145	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL, Uttar Pradesh	04/2003	230.73 399.73	03/2009 12/2008	12/2010	0/0
146	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER, West Bengal	04/2004	225.68 293.74	12/2010 12/2010	12/2010	0/0
147	REWARI-ROHTAK (NL), NR - [220100279](NR), Haryana	01/2004	149.38 330.23	02/2010 02/2011	02/2011	0/0
148	AMRAVATI-NARKHER NL(CR) - [220100118]CR, Maharashtra	06/1994	120.90 284.27	06/1999 03/2011	03/2011	0/0
149	KOTTUR-HARIHAR(NL), (SWR) - [220100212]SWR, Karnataka	04/1995	65.94 302.23	- -	03/2011	0/0
150	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR, Multi State	09/1998	925.00 -	05/2008 03/2011	03/2011	0/0
151	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR, Uttar Pradesh	04/1999	108.00 214.09	12/2009 03/2011	03/2011	0/0
152	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR, Rajasthan	04/2001	143.92 258.60	03/2011 03/2011	03/2011	0/0
153	BILASPUR-URKURA (DL) - [220100321]RVNL, Chhatisgarh	04/1997	151.52 -	- 03/2009	03/2011	0/0
154	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL, Multi State	04/2005	240.00 -	03/2009 12/2009	03/2011	0/0
155	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR, Multi State	12/2006	170.00 -	03/2011 03/2011	03/2011	0/0
156	BARDHAMAN-KATWA (GC) - [N22000091]ER, West Bengal	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011	0/0
157	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR, Gujarat	04/2006	117.36 196.95	03/2011 -	03/2011	0/0
158	MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N22000093]MRTP, Maharashtra	04/2003	3,125.20 4,174.40	06/2011 06/2011	06/2011	0/0
159	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100007]NCR, Multi State	04/1985	158.77 432.46	03/1994 -	12/2011	0/0
160	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, Orissa	04/1996	301.64 1,185.00	- 09/2009	12/2011	0/0
161	CALICUT-MANGALORE (DL) (SR) - [220100151]SR, Multi State	02/1996	240.00 -	- -	02/2012	0/0
162	KANPUR-KASGANJ-MATHURA(GC), NER - [220100197]NER, Uttar Pradesh	03/1997	395.00 1,062.36	- -	02/2012	0/0
163	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, West Bengal	04/2000	157.96 1,188.91	- 12/2009	02/2012	0/0
164	Dakshin-barasat-lakshmikantapur - [N22000116]ER, West Bengal	04/2009	259.51 533.38	12/2011 02/2012	02/2012	0/0
165	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, Andhra Pradesh	12/1994	124.43 495.68	- -	03/2012	0/0
166	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR, Orissa	04/1993	100.00 142.98	03/2002 -	03/2012	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
167	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhandd	04/1995	184.00 900.05	12/2011 12/2011	03/2012	0/0
168	KADUR-CHIKMAGALUR-SAKLSEHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	03/2012 03/2012	03/2012	0/0
169	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	02/2009 -	03/2012	0/0
170	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	- -	03/2012	0/0
171	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	03/2012 03/2012	03/2012	0/0
172	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	02/2011 02/2011	03/2012	0/0
173	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	- -	03/2012	0/0
174	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	03/2012 03/2012	03/2012	0/0
175	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	- -	03/2012	0/0
176	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	- -	03/2012	0/0
177	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	03/2010 -	03/2012	0/0
178	CONSTRUCTION OF NEW LINE FROM HARMATHI-TANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 -	- -	03/2012	0/0
179	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	03/2012 -	03/2012	0/0
180	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	03/2011 -	03/2012	0/0
181	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhandd	04/2008	167.73 -	03/2012 -	03/2012	0/0
182	Bhuj-Naliya(GC) with extension from naliya to vaylor - [N22000123]WR,Gujarat	04/2008	318.24 -	03/2012 -	03/2012	0/0
183	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 514.68	- -	06/2012	0/0
184	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]ECR,Bihar	04/1997	100.00 483.62	03/2012 03/2012	06/2012	0/0
185	CHURCHGATE-VIRAR:CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	653.84 1,302.12	06/2013 06/2012	06/2012	0/0
186	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR,Gujarat	04/2006	196.97 -	03/2011 -	06/2012	0/0
187	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	07/2012 07/2012	07/2012	0/0
188	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhandd	04/1997	194.07 -	06/2004 -	12/2012	0/0
189	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44 576.27	12/2012 -	12/2012	0/0
190	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 519.67	12/2012 12/2012	12/2012	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
191	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	03/2012 03/2012	12/2012	0/0
192	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 -	03/2012 03/2012	12/2012	0/0
193	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 -	03/2009 12/2012	12/2012	0/0
194	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 1,389.98	10/2007 12/2012	12/2012	0/0
195	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	03/2010 -	12/2012	0/0
196	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	03/1995 -	03/2013	0/0
197	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	- -	03/2013	0/0
198	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	- -	03/2013	0/0
199	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 -	- -	03/2013	0/0
200	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	- -	03/2013	0/0
201	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	03/2013 -	03/2013	0/0
202	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 -	03/2012 -	03/2013	0/0
203	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.13 -	03/2013 -	03/2013	0/0
204	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	02/2009 02/2009	04/2013	0/0
205	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	03/2009 03/2009	04/2013	0/0
206	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 -	12/2012 -	05/2013	0/0
207	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	06/2013 06/2013	06/2013	0/0
208	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	12/2011 11/2013	11/2013	0/0
209	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	- -	12/2013	0/0
210	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 -	03/2009 -	12/2013	0/0
211	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	03/2007 03/2007	03/2014	0/0
212	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 -	12/2008 -	03/2014	0/0
213	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 -	- -	03/2014	0/0
214	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 -	03/2014 -	03/2014	0/0
215	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	04/2014 -	03/2014	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
216	Jaipur - Ringus - Churu and Sikar - Loharu Gauge C - [N22000113]NWR,Rajasthan	04/2008	653.19 -	03/2014 -	03/2014	0/0
217	Suratpura - Hanumangarh - Srigananagar Gauge Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 -	03/2014 -	03/2014	0/0
218	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	03/2014 -	03/2014	0/0
219	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 -	12/2012 -	03/2014	0/0
220	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00 -	03/2010 06/2014	06/2014	0/0
221	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	- -	03/2015	0/0
222	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	12/2010 12/2010	03/2015	0/0
223	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	- -	03/2015	0/0
224	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	03/2014 03/2015	03/2015	0/0
225	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 -	- -	03/2015	0/0
226	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 -	03/2015 -	03/2015	0/0
227	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 -	03/2015 -	03/2015	0/0
228	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	04/2008 03/2014	12/2015	0/0
229	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,028.05	03/2005 12/2008	12/2015	0/0
230	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 529.23	02/2010 -	12/2015	0/0
231	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	12/2015 -	12/2015	0/0
232	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 -	03/2011 03/2014	03/2016	0/0
233	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	03/2014 03/2016	03/2016	0/0
234	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	03/2016 -	03/2016	0/0
235	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 -	03/2016 -	03/2016	0/0
236	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	06/2005 07/2011	06/2016	0/0
237	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	03/2016 -	06/2016	0/0
238	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J and K	03/1995	2,500.00 8,000.00	03/2001 -	12/2017	0/0
239	VIRAMGAM-BHILD(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	- 03/2010	-	0/0
240	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	12/2012 -	-	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
241	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	- -	-	0/0
242	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 229.88	- -	-	0/0
243	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00 -	- -	-	0/0
244	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	- -	-	0/0
245	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	- -	-	0/0
246	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 -	- -	-	0/0
247	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,045.00	- -	-	0/0
248	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 -	- -	-	0/0
249	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91 418.17	- -	-	0/0
250	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	- -	-	0/0
251	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23 -	02/2015 -	-	0/0
252	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	- -	-	0/0
253	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 -	- -	-	0/0
254	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 -	- -	-	0/0
255	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN - [N22000081]RVNL,Gujarat	09/2005	200.80 -	- -	-	0/0
256	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 -	- -	-	0/0
257	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 582.83	- -	-	0/0
258	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 -	- -	-	0/0
259	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 -	- -	-	0/0
260	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd	04/1996	371.36 -	- -	-	0/0
261	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 -	- -	-	0/0
262	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 -	- -	-	0/0
Total			64,962.90 -			0/0

Road Transport & Highways

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
263	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI, West Bengal	04/2000	273.00 -	03/2005 -	05/2012	0/0
264	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI, J and K	12/2003	193.09 -	03/2008 -	05/2012	0/0
265	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI, J and K	12/2003	166.27 -	03/2008 -	05/2012	0/0
266	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI, Uttar Pradesh	12/2003	227.00 -	12/2008 -	05/2012	0/0
267	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI, Madhya Pradesh	12/2003	225.00 -	10/2008 -	05/2012	0/0
268	SAGAR BY PASS, KM 187 TO KM 211, NH-26 (NHAI) - [240106301]NHAI, Uttar Pradesh	12/2003	151.30 -	10/2008 -	05/2012	0/0
269	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, Assam	12/2003	245.00 -	03/2008 -	05/2012	0/0
270	SALEM - U / UNDRUPET (BOT -1/TN-06) NH -68 - [N24000102]NHAI, Tamil Nadu	03/2005	941.00 -	01/2011 -	05/2012	0/0
271	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI, Karnataka	03/2005	441.00 -	- -	05/2012	0/0
272	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, Kerala	03/2005	557.00 -	02/2010 -	05/2012	0/0
273	Pune-sholapur, pkg1 - [N24000127]NHAI, Maharashtra	11/2009	1,110.00 -	05/2012 -	05/2012	0/0
274	Kishangarh-Ajmer-Beawer - [N24000128]NHAI, Rajasthan	11/2009	795.00 -	05/2012 -	05/2012	0/0
275	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI, Andhra Pradesh	08/2010	388.00 -	05/2012 -	05/2012	0/0
276	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, Assam	12/2003	157.47 -	09/2007 -	06/2012	0/0
277	Haveri-Harihar (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI, Karnataka	04/2000	241.00 -	08/2004 07/2010	06/2012	0/0
278	Harihar-Chitradurga (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI, Karnataka	04/2000	318.00 -	08/2004 -	06/2012	0/0
279	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI, Uttar Pradesh	04/2000	367.49 -	03/2005 -	06/2012	0/0
280	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI, Uttar Pradesh	12/2003	275.00 -	09/2007 -	06/2012	0/0
281	Hapur-Garhmukteswar (Others) KM.58-93, NH-24 - [240106205]NHAI, Uttar Pradesh	03/2005	220.00 -	09/2007 -	06/2012	0/0
282	Ganga Bridge to Ramdevi Crossing PH.II NH-25, KM.75-80.06 - [240106221]NHAI, Uttar Pradesh	12/2003	155.00 -	09/2008 -	06/2012	0/0
283	KOTWA TO DEWAPUR (10 LMNHP), NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI, Bihar	12/2003	240.00 -	10/2008 -	06/2012	0/0
284	ORAI TO JHANSI (UP-5), NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI, Uttar Pradesh	12/2003	340.68 -	03/2008 -	06/2012	0/0
285	Aurang-Raipur, NH-6, KM.232 TO KM.281 - [240106260]NHAI, Chhattisgarh	03/2005	190.00 -	01/2009 -	06/2012	0/0
286	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI, Assam	12/2003	225.00 -	06/2008 -	06/2012	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
287	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI, Assam	12/2003	195.00 -	06/2008 -	06/2012	0/0
288	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI, Bihar	12/2003	340.00 -	09/2008 -	06/2012	0/0
289	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00 -	06/2008 -	06/2012	0/0
290	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, Assam	12/2003	264.72 -	06/2008 -	06/2012	0/0
291	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI, West Bengal	12/2003	221.82 -	11/2008 -	06/2012	0/0
292	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, Assam	12/2003	225.00 -	06/2008 -	06/2012	0/0
293	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, Assam	12/2003	160.00 -	05/2008 -	06/2012	0/0
294	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI, Assam	12/2003	200.00 -	06/2008 -	06/2012	0/0
295	NAGPUR-KONDHALI, NH-6 (NHAI) - [N24000055]NHAI, Maharashtra	03/2005	168.00 -	12/2008 -	06/2012	0/0
296	GANJAM-ICCHAPURUM, NH-5 (NHAI) - [N24000057]NHAI, Orissa	04/2000	263.27 -	02/2004 -	06/2012	0/0
297	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI, Chhatisgarh	01/2008	464.00 -	01/2011 -	06/2012	0/0
298	MP/Maharashtra Border-Dhula - [N24000126]NHAI, Maharashtra	12/2009	835.00 -	06/2012 -	06/2012	0/0
299	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI, Multi State	04/2009	1,673.70 -	10/2011 -	06/2012	0/0
300	Surat- Dahisar (Six Lane) Km 263 to Km 502 - [N24000131]NHAI, Multi State	02/2009	1,693.75 -	08/2011 -	06/2012	0/0
301	Armur to kadloor yellareddy - [N24000143]NHAI, Andhra Pradesh	02/2010	390.56 -	02/2012 -	06/2012	0/0
302	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI, Orissa	04/2000	225.00 -	04/2004 -	07/2012	0/0
303	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI, Orissa	04/2000	228.70 -	02/2004 -	07/2012	0/0
304	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, Maharashtra	03/2005	940.00 -	07/2012 -	07/2012	0/0
305	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI, Punjab	12/2003	284.00 -	05/2008 -	08/2012	0/0
306	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI, Assam	12/2003	230.00 -	06/2005 -	09/2012	0/0
307	KOTA BYPASS, RJ-4, NH-76 (NHAI) - [240106297]NHAI, Rajasthan	12/2003	275.00 -	10/2008 -	09/2012	0/0
308	RAJMARG CHORAHA TO LAKHNANDON, KM 351 TO KM 405.7, NH-26 (NHA - [240106305]NHAI, Madhya pradesh	12/2003	229.91 -	10/2008 -	09/2012	0/0
309	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI, Gujarat	03/2010	1,509.10 -	09/2012 -	09/2012	0/0
310	LAKHNAADON TO MP/MH BORDER, KM 596.75- 653 (NS-1/BOT/MP-2), NH7 - [N24000094]NHAI, Madhya pradesh	12/2003	407.60 -	06/2010 -	10/2012	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
311	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI, Madhya Pradesh	12/2003	263.17 -	09/2009 -	10/2012	0/0
312	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI, Maharashtra	04/2010	1,170.52 -	06/2011 -	10/2012	0/0
313	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI, Andhra Pradesh	04/2010	1,740.00 -	10/2012 -	10/2012	0/0
314	THANJAUR-TRICHY, NH-67 (NHAI) - [N24000056]NHAI, Tamil Nadu	03/2005	280.00 -	06/2009 -	11/2012	0/0
315	WADNER-DEVDHARI (NS-60/MH) (KM 94-123 KM) - [N24000150]NHAI, Maharashtra	02/2011	193.45 -	11/2012 -	11/2012	0/0
316	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI, Bihar	12/2003	300.00 -	10/2008 -	12/2012	0/0
317	BIJNI TO ASSAM /WB. BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI, Assam	12/2003	237.80 -	06/2008 -	12/2012	0/0
318	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI, Bihar	12/2003	332.94 -	09/2008 -	12/2012	0/0
319	SAGAR - RAJMARG CHORAHA, KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI, Madhya Pradesh	12/2003	203.43 -	10/2008 -	12/2012	0/0
320	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, Madhya Pradesh	12/2003	251.03 -	10/2008 -	12/2012	0/0
321	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, West Bengal	12/2003	225.00 -	07/2008 -	12/2012	0/0
322	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, Assam	12/2003	175.96 -	04/2008 -	12/2012	0/0
323	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, Assam	12/2003	198.16 -	04/2008 -	12/2012	0/0
324	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00 -	04/2008 -	12/2012	0/0
325	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, Assam	12/2003	217.61 -	04/2010 -	12/2012	0/0
326	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI, Madhya Pradesh	12/2003	300.93 -	10/2009 -	12/2012	0/0
327	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, Multi State	12/2003	604.00 -	12/2009 -	12/2012	0/0
328	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI, Uttar Pradesh	12/2003	355.06 -	09/2009 -	12/2012	0/0
329	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI, Multi State	12/2003	232.45 -	09/2010 -	12/2012	0/0
330	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, Haryana	04/2007	486.00 -	05/2010 -	12/2012	0/0
331	Jaipur-Tonk-Deoli - [N24000135]NHAI, Rajasthan	06/2010	792.06 -	12/2012 -	12/2012	0/0
332	Hazaribagh-Ranchi - [N24000141]NHAI, Jharkhand	08/2010	625.07 -	01/2013 -	01/2013	0/0
333	BHOPAL-SANCHI - [N24000192]NHAI, Madhya Pradesh	10/2011	209.00 -	01/2013 -	01/2013	0/0
334	PATNA-MUZZAFFARPUR - [N24000165]NHAI, Bihar	08/2010	671.30 -	02/2013 -	02/2013	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
335	JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan	08/2010	267.81 -	02/2013 -	02/2013	0/0
336	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	02/2009 -	03/2013	0/0
337	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	04/2009 -	03/2013	0/0
338	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00 -	07/2010 -	03/2013	0/0
339	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00 -	03/2013 -	03/2013	0/0
340	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55 -	03/2013 -	03/2013	0/0
341	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,Gujarat	09/2010	805.39 -	03/2013 -	03/2013	0/0
342	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,Multi State	09/2011	754.00 -	03/2013 -	03/2013	0/0
343	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh	10/2010	1,175.00 -	04/2013 -	04/2013	0/0
344	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00 -	05/2013 -	05/2013	0/0
345	Trichy Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00 -	05/2013 -	05/2013	0/0
346	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16 -	09/2007 -	06/2013	0/0
347	Chikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30 -	10/2011 -	06/2013	0/0
348	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00 -	11/2011 -	06/2013	0/0
349	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00 -	11/2012 -	06/2013	0/0
350	MURADABAD-BAREILLY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00 -	06/2013 -	06/2013	0/0
351	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50 -	06/2013 -	06/2013	0/0
352	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu	06/2011	600.00 -	06/2013 -	06/2013	0/0
353	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81 -	04/2009 -	07/2013	0/0
354	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04 -	11/2008 -	07/2013	0/0
355	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	953.00 -	07/2013 -	07/2013	0/0
356	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88 -	07/2013 -	07/2013	0/0
357	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,Bihar	01/2011	575.00 -	07/2013 -	07/2013	0/0
358	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat	03/2011	785.50 -	08/2013 -	08/2013	0/0
359	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00 -	08/2013 -	08/2013	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
360	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00 -	08/2013 -	08/2013	0/0
361	BHUBANESWAR TO PURI - [N24000195]NHAI,Orissa	03/2011	500.29 -	08/2013 -	08/2013	0/0
362	4-laning of Faraka-Raiganj - [N24000202]NHAI,Multi State	02/2011	1,078.84 -	08/2013 -	08/2013	0/0
363	4-laning of Brahampore-Faraka - [N24000203]NHAI,Multi State	02/2011	998.79 -	08/2013 -	08/2013	0/0
364	4-laning of Raiganj-Dalkola - [N24000204]NHAI,Multi State	02/2011	580.43 -	08/2013 -	08/2013	0/0
365	New 4 Lane elevated road from chennai airport - [N24000139]NHAI,Tamil Nadu	09/2010	1,655.00 -	09/2013 -	09/2013	0/0
366	BAREILY-SITAPUR - [N24000200]NHAI,Uttar Pradesh	03/2011	1,046.00 -	09/2013 -	09/2013	0/0
367	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00 -	08/2012 -	10/2013	0/0
368	Tirupati - Chennai - [N24000178]NHAI,Tamil Nadu	04/2011	571.00 -	10/2013 -	10/2013	0/0
369	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00 -	11/2013 -	11/2013	0/0
370	ROHTAK-BAWAL - [N24000169]NHAI,Haryana	05/2011	650.00 -	11/2013 -	11/2013	0/0
371	Muzafarpur - Sonbarsa - [N24000174]NHAI,Bihar	05/2011	511.54 -	11/2013 -	11/2013	0/0
372	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,Bihar	05/2011	511.54 -	11/2013 -	11/2013	0/0
373	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	02/2010 -	12/2013	0/0
374	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI,Tamil Nadu	06/2011	535.00 -	12/2013 -	12/2013	0/0
375	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM. - [N24000172]NHAI,Tamil Nadu	09/2011	1,250.00 -	12/2013 -	12/2013	0/0
376	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	11/2008 -	01/2014	0/0
377	JORBAT - BARAPANI - [N24000180]NHAI,Meghalaya	01/2011	536.00 -	01/2014 -	01/2014	0/0
378	PUNE-SHOLAPUR,Pkg-II - [N24000193]NHAI,Maharashtra	09/2011	835.00 -	01/2014 -	01/2014	0/0
379	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,Orissa	07/2011	586.00 -	01/2014 -	01/2014	0/0
380	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00 -	05/2013 -	02/2014	0/0
381	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,Meghalaya	02/2011	226.00 -	02/2014 -	02/2014	0/0
382	4-laning of Barhi-Hazaribagh - [N24000191]NHAI,Jharkhandd	02/2012	398.00 -	02/2014 -	02/2014	0/0
383	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37 -	10/2011 -	03/2014	0/0
384	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54 -	05/2013 -	03/2014	0/0
385	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,Multi State	09/2011	2,848.00 -	03/2014 -	03/2014	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
386	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,Bihar	09/2011	574.00 -	03/2014 -	03/2014	0/0
387	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00 -	09/2007 -	04/2014	0/0
388	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	07/2009 -	04/2014	0/0
389	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00 -	02/2014 -	04/2014	0/0
390	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,Bihar	10/2011	375.09 -	04/2014 -	04/2014	0/0
391	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI,Andhra Pradesh	11/2011	1,535.00 -	05/2014 -	05/2014	0/0
392	2laning with PS Gopalganj-Chappra - [N24000190]NHAI,Bihar	12/2011	325.00 -	05/2014 -	05/2014	0/0
393	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,Orissa	11/2011	909.00 -	05/2014 -	05/2014	0/0
394	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,J and K	07/2010	1,813.76 -	07/2013 -	06/2014	0/0
395	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,Rajasthan	12/2011	2,388.00 -	06/2014 -	06/2014	0/0
396	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]NHAI,Multi State	12/2011	1,047.00 -	06/2014 -	06/2014	0/0
397	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00 -	09/2013 -	07/2014	0/0
398	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	08/2014 -	08/2014	0/0
399	PANIKHOLI-RIMOLI - [N24000197]NHAI,Orissa	03/2012	1,410.00 -	09/2014 -	09/2014	0/0
400	PANIPAT-ROHTAK - [N24000151]NHAI,Haryana	04/2011	807.00 -	10/2014 -	10/2014	0/0
401	NASHRI CHANANI - [N24000162]NHAI,J and K	06/2010	2,159.00 -	06/2015 -	06/2015	0/0
402	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,J and K	07/2010	1,987.00 -	07/2015 -	07/2015	0/0
403	SNG toBANL - [N24000189]NHAI,J and K	06/2011	1,100.70 -	06/2014 -	-	0/0
Total			88,064.60 -			0/0
<u>Shipping & Ports</u>						
404	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	10/2008 -	10/2008	0/0
405	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 -	10/2008 -	10/2008	0/0
406	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	04/2009 11/2009	02/2011	0/0
407	MARINE LIQUID TERMINALS - [N25000054]ENNORE TANK,Tamil Nadu	10/2004	196.25 -	06/2006 09/2011	09/2011	0/0
408	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 252.00	03/2012 -	03/2012	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
409	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	04/2011 06/2011	06/2012	0/0
410	Acquisition of two nos. of 120 B.P BY 079& 080 - [N25000042]SHIPP.,Maharashtra	04/2009	290.85 -	06/2011 06/2012	06/2012	0/0
411	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	12/2011 08/2012	08/2012	0/0
412	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91 -	09/2012 -	09/2012	0/0
413	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	01/2012 09/2012	09/2012	0/0
414	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	06/2010 -	11/2012	0/0
415	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	12/2010 -	12/2012	0/0
416	CONSTRUCTION OF Berthing and Allied Facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	02/2011 -	12/2012	0/0
417	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 627.64	12/2012 -	12/2012	0/0
418	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	03/2011 -	03/2013	0/0
419	SETTING UP OF SINGLE POINT MOORING (SPM) - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -	05/2013 -	03/2013	0/0
420	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 600.00	03/2006 -	12/2013	0/0
421	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	12/2013 -	12/2013	0/0
422	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	02/2014 -	02/2014	0/0
423	DEVELOPMENT OF COAL TERMINAL - [N25000055]ENNORE PORT LTD,Tamil Nadu	09/2006	399.13 -	08/2010 -	-	0/0
424	DEVELOPMENT OF IRON ORE TERMINAL - [N25000056]ENNORE PORT LTD,Tamil Nadu	09/2006	370.00 -	08/2010 -	-	0/0
	Total		17,053.06 -			0/0
Telecommunications						
425	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	03/2010 -	10/2010	0/0
426	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84 -	10/2009 -	03/2011	0/0
427	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	02/2007 12/2010	08/2011	0/0
428	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	02/2007 03/2011	03/2012	0/0
429	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 930.60	11/2010 -	03/2012	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
430	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00 -	12/2005 03/2008	05/2012	0/0
431	NIB Project Capacity Expansion - [N26000098]BSNL,Multi State	06/2007	175.52 -	12/2008 -	05/2012	0/0
432	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	12/2008 -	06/2012	0/0
433	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	06/2009 -	06/2012	0/0
434	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	01/2009 -	06/2012	0/0
435	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhandd	03/2008	328.13 -	03/2009 -	06/2012	0/0
436	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	10/2010 03/2012	07/2012	0/0
437	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38 -	10/2007 -	-	0/0
438	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00 -	03/2009 -	-	0/0
439	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	03/2010 -	-	0/0
	Total		6,161.00 -			0/0
Urban Development						
440	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00 -	09/2014 -	09/2014	0/0
441	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00 -	03/2016 -	03/2016	0/0
442	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	04/2009 -	-	0/0
	Total		37,850.18 -			0/0
Water Resources						
443	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	12/2007 -	12/2012	0/0
	Total		542.90 -			0/0
Grand Total			443,217.59			0/0

Abbreviations used in the report

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro
LEP	Life Extension Program
LOI	Letter of Intent

LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECF	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SSS	Sardar Swaran Singh
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
