

**329th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹ 150 crore and above)
April 2013**



NHAI - SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5)



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro
LEP	Life Extension Program

LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

Contents

Executive Summary in Hindi	1 -5
Executive Summary in English	6-11
Month wise list of completed projects Costing Rs. 1000 Crore and Above During 2010-11	2-14
Summary of Projects	15-28
Trend and Graphical Analysis of Projects	29-41
Sector wise analysis of projects	42-42
List of All Ongoing Projects	43-70
Sector wise Graph	71-83
ANNEXURE	84-84
Central Sector Projects	85-85
List of Projects Having Expenditure More than cost	86-91
List of Projects Ahead of Schedule	92-92
List of Projects with out Original date of Commissioning	93-95
List of Projects with out date of Commissioning	96-100
List of On schedule Projects	101-109
List of Projects without Milestones	110-127
List of Delayed Projects w.r.t Original and Revised	128-148
List of Projects Having cost overrun w.r.t original	149-158
List of Projects Having cost and time overrun w.r.t original	159-163
Abbreviations	164-165

कार्यकारी सारांश

अप्रैल, 2013 की फ्लैश रिपोर्ट में 150 करोड़ रुपए और उससे अधिक लागत वाली केन्द्रीय क्षेत्र की 566 अवसंरचनात्मक परियोजनाओं की स्थिति दी गई है। अप्रैल, 2013 के दौरान 3 परियोजनाओं (रेलवे की 2 परियोजनाओं तथा विद्युत क्षेत्र की 1 परियोजना) के पूरा होने की सूचना दी गई है।

2. संदर्भाधीन माह के दौरान, 566 परियोजनाओं में से 261 परियोजनाओं में नवीनतम समय-सारणी की तुलना में विलंब हुआ तथा 53 परियोजनाओं के संबंध में पिछले माह में सूचित की गई समापन की तारीख की तुलना में अतिरिक्त विलंब की सूचना दी गई है। इन 53 परियोजनाओं में से, 19 परियोजनाएं 1000 करोड़ रु. और अधिक लागत वाली बड़ी परियोजनाएं हैं। इस्पात, कोयला, दूरसंचार, पोत परिवहन तथा पत्तन, रेलवे, पेट्रोलियम, विद्युत, तथा सड़क परिवहन एवं राजमार्ग क्षेत्रों से संबंधित परियोजनाओं के संबंध में 1 से 24 महीनों तक का अतिरिक्त विलंब हुआ है।

क्र.सं.	क्षेत्र	निगरानी के तहत आने वाली परियोजनाएं	नवीनतम समय-सारणी की तुलना में विलंबित परियोजनाएं	रिपोर्ट वाले माह के दौरान अतिरिक्त विलंबित परियोजनाएं	अतिरिक्त विलंबित बड़ी परियोजनाएं
1.	सड़क परिवहन एवं राजमार्ग	149	88	13	0
2.	रेलवे	129	31	5	2
3.	विद्युत	100	51	16	9
4.	पेट्रोलियम	70	38	7	5
5.	कोयला	52	29	2	1
6.	पोत परिवहन एवं पत्तन	19	2	5	2
7.	इस्पात	17	13	1	0
8.	दूरसंचार	13	5	4	0
9.	नागर विमानन	6	2	0	0
10.	परमाणु ऊर्जा	4	2	0	0
11.	शहरी विकास	4	0	0	0
12.	उर्वरक	1	0	0	0
13.	पेट्रोरसायन	1	0	0	0
14.	जल संसाधन	1	0	0	0
कुल		566	261	53	19

3. 566 परियोजनाओं के कार्यान्वयन की कुल मूल लागत लगभग 7,98,047.83 करोड़ रुपए थी तथा उनके पूरा होने की अनुमानित लागत 9,43,167.88 करोड़ रुपए होने की संभावना है जो 1,45,120.05 करोड़ रुपए (मूल लागत का 18.20%) की समग्र लागत वृद्धि को दर्शाता है। अप्रैल, 2013 तक इन परियोजनाओं पर किया गया व्यय 4,56,277.05 करोड़ रुपए है जो परियोजनाओं की अनुमानित लागत का 48.40% है। लागतवृद्धि की अधिकतम प्रतिशतता वाली 5 परियोजनाएं नीचे दी गई हैं:-

लागतवृद्धि की अधिकतम प्रतिशतता वाली 5 परियोजनाओं की सूची (30.04.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (रु. करोड़)			लागत-वृद्धि (% में)
				मूल	संशोधित	अनुमानित	
1	नांगल बांध तलवारा (एनएल), एनआर	रेलवे	03/1981	37.68	450.00	1036.78	2651.54
2	गाजोले-ईटाहार सहित इकलाखी से बलूरघाट तक नई बी जी लाइन रेलवे लाइन (एनएल) एनईएफआर	रेलवे	04/1983	36.80	274.41	703.17	1810.79
3	हावड़ा-आमता-चेपादंगा एनएल (एसईआर)	रेलवे	04/1974	31.42	393.46	535.40	1604.01
4	बांकुरा-दामोदर (जीसी) (एसईआर)	रेलवे	03/1998	111.90	1028.05	1423.98	1172.55
5	रूपसा-बांगरीपोसी (जीसी) (एसईआर)	रेलवे	02/1996	57.94	604.04	639.97	1004.54

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

4. वास्तविक अर्थ में अधिकतम लागतवृद्धि वाली 5 परियोजनाएं निम्नानुसार हैं:-

अधिकतम लागतवृद्धि वाली 5 परियोजनाओं की सूची (30.04.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (रु. करोड़)		
				मूल लागत	अनुमानित लागत	लागत-वृद्धि
1	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	2500.00	20000.00	17500.00
2	बंगलौर मेट्रो रेल परियोजना	शहरी विकास	05/2006	6395.00	11609.00	5214.00
3	सुबानश्री लोअर एचईपी (एनपीसीआईएल)	विद्युत	09/2003	6285.33	10667.00	4381.67
4	कुंडकुलम एपीपी (एनपीसीआईएल)	परमाणु ऊर्जा	12/2001	13171.00	17270.00	4099.00
5	बी पुत्र ब्रिज एवं बोगीबिल एंड लिंक लाईन्स एनईएफआर	रेलवे	09/1997	1000.00	4996.65	3996.65

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

5. 566 परियोजनाओं में से, 2 परियोजनाएं समय से पहले चल रही हैं, 162 समय पर तथा 261 परियोजनाएं नवीनतम समय-सारणी की तुलना में विलंबित हैं । तथापि, विलंबित परियोजनाओं की संख्या 273 तक और बढ़ जाती है यदि समापन की मूल समय-सारणी के आधार पर गणना की जाती है । इसके अलावा, 17 परियोजनाएं किसी आरंभ संबंधी समय-सारणी/तारीख के बिना स्वीकृत की गई हैं तथा 124 परियोजनाओं के संबंध में न तो शुरू करने का वर्ष और न परियोजना के अनुमानित रूप से पूरा होने का समय सूचित किया गया है । 261 विलंबित परियोजनाओं में से, 64 परियोजनाओं में 1 से 12 माह तक का विलंब हुआ, 68 परियोजनाओं में 13 से 24 महीने तक का विलंब हुआ, 79 परियोजनाओं में 25 से 60 माह तक का विलंब हुआ तथा 56 परियोजनाओं में 61 माह और उससे अधिक का विलंब हुआ । अधिकतम विलंब वाली 5 परियोजनाएं नीचे दी गई हैं:-

अधिकतम समयवृद्धि वाली 5 परियोजनाओं की सूची (30.04.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	शुरू करने की तारीख		समय-वृद्धि (महीने में)
				मूल	अनुमानित	
1	गुना-इटावा बरास्ता शिवपुरी-ग्वालियर-भिंड एनएलए(एनसीआर)	रेलवे	04/1986	03/1994	10/2013	235
2	फ्रेट आप्रेशनस इन्फोर्मेशन सिस्टम (एफओआईएस)	रेलवे	03/1984	03/1995	03/2013	216
3	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	03/2001	12/2017	201
4	बांकुरा-दामोदर (जीसी) (एसईआर)	रेलवे	03/1998	03/2005	06/2016	135
5	लांझीगढ़-जूनागढ़ एनएल (ईसीओआर)	रेलवे	04/1993	03/2002	03/2013	132

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक समयवृद्धि से बचने के लिए इन परियोजनाओं की समीक्षा करेंगे ।

6. विभिन्न परियोजना कार्यान्वयन एजेंसियों द्वारा यथा सूचित समयवृद्धि के संक्षिप्त कारणों में भूमि अधिग्रहण, वन संबंधी स्वीकृति में विलंब, उपस्करों के संस्थापन में विलम्ब, सामग्री की आपूर्ति में विलंब, भू वैज्ञानिक गतिविधियां, कार्यक्षेत्र में परिवर्तन, आरओयू/आरओडब्ल्यू समस्याएं, कानून और व्यवस्था आदि शामिल हैं ।

7. मंत्रालय के ऑनलाइन कम्प्यूटरीकृत मॉनीटरिंग सिस्टम (ओसीएमएस) में विभिन्न अवसंरचना परियोजनाओं के पीईआरटी चार्टों से तैयार किए गए लक्ष्यों की निगरानी की परिकल्पना की गई है । परियोजना प्राधिकारियों से नियमित रूप से अनुरोध किया गया है कि वे बेहतर निगरानी को सुचारू बनाने के लिए प्रत्येक परियोजना के संबंध में उपलब्धियों की सूची की प्रविष्टि करें । तथापि, सभी परियोजना एजेंसियां उपलब्धियों की सूची प्रदान नहीं कर रही हैं । पहले शुरू की गई 5 परियोजनाओं जिनके लक्ष्य परियोजना एजेंसियों द्वारा प्रदान नहीं किए जा रहे हैं, नीचे दिए गए हैं:-

बिना उपलब्धियों वाली पहली 5 परियोजनाओं की सूची (30.04.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (करोड़ रु.)		संचयी व्यय (करोड़ रु.)	शुरू करने की तारीख		उपलब्धि
				मूल	अनुमानित		मूल	अनुमानित	
1	हावड़ा-आमता-चंपादंगा एनएल (एससीआर)	रेलवे	04/1974	31.42	535.40	176.52	03/2007	03/2015	एन.आर.
2	नांगल बांध तलवारा (एनएल), एनआर	रेलवे	03/1981	37.68	1036.78	353.41	07/2012	एन.आर.	एन.आर.
3	इकलाखी से बलूरघाट तक नई बी जी लाइन रेलवे लाइन (एनएल) एनईएफआर	रेलवे	04/1983	36.80	703.17	247.74	एन.आर.	03/2015	एन.आर.
4	फ्रेट आप्रेशनस इन्फोर्मेशन सिस्टम (एफओआईएस)	रेलवे	03/1984	520.00	634.13	555.27	03/1995	03/2013	एन.आर.
5	तामलुक दीघा, लाइन का दोहरीकरण (एसईआर)	रेलवे	03/1984	293.97	1074.47	433.89	06/2005	06/2016	एन.आर.

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार लक्ष्यों को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

एन.आर.: सूचित नहीं ।

8. यह पाया गया है कि परियोजना एजेंसियां संशोधित लागत अनुमानों तथा अनेक परियोजनाओं को शुरू करने की समय-सारणी को सूचित नहीं कर रही हैं, जो संकेत देता है कि समय/लागतवृद्धि संबंधी आंकड़े कम बताए गए हैं । पहले शुरू की गई 5 परियोजनाएं जिनमें परियोजना एजेंसियां संशोधित लागत अनुमानों की सूचना नहीं दे रही हैं/को प्रदान नहीं करा रही हैं, नीचे दिए गए हैं:-

बिना संशोधित लागत अनुमानों वाली पहली 5 परियोजनाओं की सूची (30.04.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (करोड़ रु.)		संचयी व्यय (करोड़ रु.)
				मूल	संशोधित	
1	लांझीगढ़-जूनागढ़ एनएल (ईसीओआर)	रेलवे	04/1993	100.00	142.98	211.19
2	अमरावती-नरखेर एनएल (सीआर)	रेलवे	06/1994	120.90	284.27	541.95
3	पेड़ापल्ली-करीमनगर-निजामाबाद एनएल (एससीआर)	रेलवे	12/1994	124.43	495.68	597.99
4	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	2500.00	2500.00	8549.43
5	कोटूर-हरीहर (एनएल), (एसडब्ल्यूआर)	रेलवे	04/1995	65.94	302.23	344.29

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार संशोधित लागत अनुमानों को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

पहले शुरू की गई 5 परियोजनाएं जिनमें परियोजना एजेंसियां शुरू करने की संशोधित समय-सारणी की सूचना नहीं दे रही हैं/को प्रदान नहीं करा रही हैं, नीचे दिए गए हैं:-

शुरू करने की संशोधित समय-सारणी के बिना पहली 5 परियोजनाओं की सूची (30.04.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना को शुरू करने की तारीख		
				मूल	संशोधित	अनुमानित
1	नांगल बांध-तलवारा (एनएल), एनआर	रेलवे	03/1981	07/2012	एन.आर.	एन.आर.
2	विरमगाम-भिल्डी (डब्ल्यूआर), जीसी	रेलवे	04/1990	एन.आर.	03/2010	एन.आर.
3	अमरावती-नरखेर एनएल (सीआर)	रेलवे	06/1994	06/1999	03/2011	03/2011
4	पेड़ापल्ली-करीमनगर-निजामाबाद एनएल (एससीआर)	रेलवे	12/1994	एन.आर.	एन.आर.	03/2012

5	कोटर-हरीहर (एनएल), (एसडब्ल्यूआर)	रेलवे	04/1995	एन.आर.	एन.आर.	12/2012
---	-------------------------------------	-------	---------	--------	--------	---------

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार शुरू करने की संशोधित समय-सारणी को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

एन.आर.: सूचित नहीं।

9. विलंब/अतिरिक्त विलंब का क्षेत्र-वार ब्यौरा निम्नानुसार है :-

(i) **इस्पात क्षेत्र** में, 17 परियोजनाओं में से 13 परियोजनाएं विलंबित हैं। माह के दौरान "बेलाडिला आयरन ओर प्रोजेक्ट डिपोजिट-11 बी, एनएमडीसी" परियोजना के संबंध में 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है जिनमें से 2 मेगा परियोजनाएं हैं। तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है।

(ii) **कोयला क्षेत्र** में, 52 परियोजनाओं में से 29 परियोजनाएं विलंबित हैं। माह के दौरान 02 परियोजनाओं के संबंध में क्रमशः 4 और 12 माह के अतिरिक्त विलंब की सूचना दी है जिनमें से 1 मेगा परियोजना है। 'कृष्णशीला (4 एमटीवाई), एनसीएल' परियोजना के संबंध में वन विभाग से स्वीकृति मिलने में विलम्ब के कारण 12 माह के अतिरिक्त विलंब की सूचना दी गई है। 'नेवेली न्यू थर्मल पावर प्रोजेक्ट (2X500 मेगावाट), एनएलसी परियोजना के संबंध में 4 माह के अतिरिक्त विलंब की सूचना दी गई है। तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है।

(iii) **दूरसंचार क्षेत्र** में, 13 परियोजनाओं में से, 5 परियोजनाएं विलंबित हैं। माह के दौरान, 4 परियोजनाओं में 2-3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। '283000 लाइन्स (2 जी) तथा 75000 लाइन्स, बीएसएनएल के जीएसएम उपस्कर' तथा 'असम टेलीकाम सर्किल फेज -VI 2जी तथा 3जी, बीएसएनएल' परियोजनाओं के संबंध में विपरीत मौसम परिस्थितियों तथा स्थानीय निकायों में फाइबर केबल बिछाने की अनुमति मिलने में विलंब के कारण क्रमशः प्रत्येक में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 'टर्नकी आधार पर बीएसएनएल में ईआरपी, बीएसएनएल' परियोजना में कार्य प्रक्रिया के बदलाव तथा बिक्री से संबंधित विभिन्न मुद्दों के कारण 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 'सप्लाई इंस्टोलेशन टेस्टिंग एंड कमिशनिंग ऑफ रूरल वाईमैक्स, बीएसएनएल परियोजना के संबंध में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। तथापि, इन परियोजनाओं में विलंब के लिए परियोजना अधिकारियों द्वारा कोई विशेष कारण नहीं बताया गया है।

(iv) **पोत परिवहन तथा पत्तन क्षेत्र** में, 19 परियोजनाओं में से 2 परियोजनाएं विलंबित हैं। माह के दौरान, 5 परियोजनाओं के संबंध में 1-10 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। ये दोनों परियोजनाएं मेगा परियोजनाएं हैं। 5 परियोजनाओं में से 2 परियोजनाओं के संबंध में क्रमशः 1 और 2 माह के अतिरिक्त विलंब की सूचना दी गई है; पुथु, पोर्ट ट्रस्ट में एलएनजी रिगैसिफिकेशन टर्मिनल की स्थापना और 6 एंकर हैंडलिंग टग कम सप्लाई, शिपिंग कार्पोरेशन ऑफ इंडिया के अधिग्रहण तथा 4 एंकर हैंडलिंग टग कम सप्लाई, शिपिंग कॉरपोरेशन ऑफ इंडिया के अधिग्रहण से क्रमशः 3, 5 और 10 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। तथापि, इन परियोजनाओं में विलम्ब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है।

(v) **रेलवे क्षेत्र** में, 124 परियोजनाओं में से 31 परियोजनाएं विलंबित हैं। माह के दौरान, 5 परियोजनाओं के संबंध में 1-24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है जिनमें से 2 बड़ी परियोजनाएं हैं। 5 परियोजनाओं में से, 2 परियोजनाओं के संबंध में क्रमशः 1 माह तथा 3 माह के अतिरिक्त विलंब की सूचना दी गई है तथा 'बेलचेरी से स्टेशन थॉमस तक एमआरटीएस' का विस्तार एमटीपी, एमआरटीपी परियोजना के संबंध में संविदात्मक मुद्दे के कारण 9 माह के अतिरिक्त विलम्ब की सूचना प्राप्त हुई है। 'बेलापुर-सीवुड उरेन इलेक्ट्रीफाइड डबल लाइन (एमटीपी), एमआरटीपी' के संबंध में प्रतिबंधित फंड के कारण 24 माह के अतिरिक्त विलंब की सूचना दी गई है। 'मुंबई अर्बन ट्रांसपोर्ट प्रोजेक्ट फेज-II, एमआरटीपी' परियोजना के संबंध में 9 माह के अतिरिक्त विलम्ब की सूचना दी गई है। तथापि, परियोजना प्राधिकारियों द्वारा इन परियोजनाओं में विलंब के लिए कोई विशेष कारण नहीं बताया गया है।

(vi) **पेट्रोलियम क्षेत्र** में, 70 परियोजनाओं में से 38 परियोजनाएं विलंबित हैं। माह के दौरान, 7 परियोजनाओं के संबंध में 1-2 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें 5 बड़ी परियोजनाएं हैं। इन 7 परियोजनाओं में से, 2 परियोजनाओं के संबंध में प्रत्येक में 1 माह के अतिरिक्त विलम्ब की सूचना दी गई है। 'डेवलपमेंट ऑफ सी-सीरीज फील्ड्स, ओएनजीसी' तथा 'डेवलपमेंट ऑफ बी-22 कलस्टर फील्ड्स, ओएनजीसी' परियोजनाओं के संबंध में क्रमशः स्थल के फिर से चयन करने तथा अदालत संबंधी मामलों में देरी के कारण 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'बुटाडीन एक्सट्रैक्शन यूनिट (बीडीईयू) एट पनिपा, आईओसीएल' तथा 'बीएचई तथा बीएच-35 एरिया, ओएनजीसी के विकास' के संबंध में क्रमशः संविदात्मक मुद्दों तथा कार्यों में देरी के कारण प्रत्येक में 2 माह के अतिरिक्त विलम्ब की सूचना प्राप्त हुई है। 'हाइड्रोक्रैकर रीवैम्प एंड सेटिंग अप ऑफ न्यू सीसीआर एट मुंबई, बीपीसीएल' में 2 माह के अतिरिक्त विलम्ब की सूचना प्राप्त हुई है। तथापि, परियोजना प्राधिकारियों द्वारा इन परियोजनाओं में विलंब के लिए कोई विशेष कारण नहीं बताया गया है।

(vii) **विद्युत क्षेत्र** में, 100 परियोजनाओं में से 51 परियोजनाएं विलंबित हैं। माह के दौरान 16 परियोजनाओं के संबंध में 1-13 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है, इनमें से 9 मेगा परियोजनाएं हैं। इन 16 परियोजनाओं में से 2 परियोजना के संबंध में प्रत्येक में 1 माह के अतिरिक्त

विलंब की सूचना प्राप्त हुई है, 2 परियोजना के संबंध में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है तथा 5 परियोजनाओं के संबंध में प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है तथा 2 परियोजनाओं में प्रत्येक में 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, 'ट्रांसमिशन सिस्टम फार ट्रांसफर ऑफ पावर फ्रॉम जेनरेशन, पीजीसीआईएल' तथा 'इस्टर्न रिजन ट्रांसमिशन सिस्टम-III, पीजीसीआईएल' संबंधी परियोजनाओं में भूमि अधिग्रहण में विलंब होने के कारण प्रत्येक में 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। परियोजना, फेज-I जनरेशन परियोजना के लिए पारेषण प्रणाली, पीजीसीआईएल' तथा जेनरेशन-पार्ट बी से विद्युत परिवर्तन के पारेषण प्रणाली के संबंध में क्रमशः भूमि अधिग्रहण में देरी के कारण प्रत्येक 10 और 13 माह के अतिरिक्त विलम्ब की सूचना प्राप्त हुई है। 'विंध्याचल-IV तथा रिहन्द-I की पारेषण प्रणाली, पीजीसीआईएल' परियोजना के संबंध में वन संबंधी स्वीकृति मिलने में देरी के कारण 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है।

(vii) सड़क परिवहन एवं राजमार्ग क्षेत्र में, 149 परियोजनाओं में से 88 परियोजनाएं विलंबित हैं। माह के दौरान 13 परियोजनाओं के संबंध में 1-18 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। इन 13 परियोजनाओं में से, 6 परियोजनाओं के संबंध में प्रत्येक में 1 माह, 4 परियोजनाओं के संबंध में प्रत्येक में 2 माह; 'त्रिची-कोरूर एनएच-67, एनएचएआई' तथा गंगा ब्रिज से रामदेवी क्रासिंग फेज-II एनएच-25, 75-80 किमी, एनएचएआई' परियोजनाओं के संबंध में क्रमशः 6 माह और 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 'डिंडीगुल-कुमली एनएचएआई' परियोजना के संबंध में 18 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। परियोजना कार्यान्वयन एजेंसी ने इन परियोजनाओं में विलम्ब के लिए किसी विशेष कारण का उल्लेख नहीं किया है। तथापि, इन परियोजनाओं में विलम्ब के कारण भूमि अधिग्रहण में विलम्ब, वन तथा पर्यावरण संबंधी स्वीकृति में विलम्ब, जनोपयोगी सुविधाओं के प्रतिस्थापन की समस्या, ठेकेदारों का घटिया कार्य निष्पादन आदि हैं।

10. दिनांक 30.04.2013 की स्थिति के अनुसार, विभिन्न क्षेत्रों में 150 करोड़ रुपए तथा अधिक लागत वाली परियोजनाओं के संबंध में स्थिति रिपोर्ट में दर्शाई गई है।

11. इसे सचिव, सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय का अनुमोदन प्राप्त है।

EXECUTIVE SUMMARY

1. The Flash Report for April 2013 contains information on the status of the 566 Central Sector Infrastructure Projects costing ₹ 150 crore and above. During April 2013, 3 projects (2 projects in Railways and 1 project in Power Sector) have reported completion.

2. During the reference month, out of 566 projects, 261 projects are delayed with respect to latest schedule and 53 projects have reported additional delays vis-à-vis the date of completion reported in the previous month. Of these 53 projects, 19 are Mega Projects costing ₹ 1000 crore and above. The additional delays are in the range of 1 to 24 months in respect of projects relating to Steel, Coal, Telecommunication, Shipping & Ports, Railways, Petroleum, Power and Road Transport & Highways Sectors.

S. No.	Sector	Projects on monitor	Delayed Projects w.r.t latest schedule	Additionally delayed during the month under report	Additionally delayed Mega Projects
1.	Road Transport & Highways	149	88	13	0
2.	Railways	129	31	5	2
3.	Power	100	51	16	9
4.	Petroleum	70	38	7	5
5.	Coal	52	29	2	1
6.	Shipping & Ports	19	2	5	2
7.	Steel	17	13	1	0
8.	Telecommunications	13	5	4	0
9.	Civil Aviation	6	2	0	0
10.	Atomic Energy	4	2	0	0
11.	Urban Development	4	0	0	0
12.	Fertilizers	1	0	0	0
13.	Petrochemicals	1	0	0	0
14.	Water Resources	1	0	0	0
Total		566	261	53	19

3. Total original cost of implementation of the 566 projects was about ₹ 7,98,047.83 crore and their anticipated completion cost is likely to be ₹ 9,43,167.88 crore, which reflects an overall cost overruns of ₹ 1,45,120.05 crore (18.20 % of original cost). The expenditure incurred on these projects till April 2013 is ₹ 4,56,277.05 crore, which is 48.40 % of the anticipated cost of the projects. The 5 projects with the maximum percentage cost overruns are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM PERCENTAGE COST OVERRUNS (as on 30-04-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹ ; crore)			COST OVERRUNS (in %)
				ORIGINAL	REVISED	ANTICIPATED	
1	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	37.68	450.00	1036.78	2651.54
2	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	Railways	04/1983	36.80	274.41	703.17	1810.79
3	HOWRAH-AMTA-CHAMPADANGA NL (SER)	Railways	04/1974	31.42	393.46	535.40	1604.01
4	BANKURA - DAMODAR (GC) (SER)	Railways	03/1998	111.90	1028.05	1423.98	1172.55
5	RUPSA-BANGRIPOSI (GC) (SER)	Railways	02/1996	57.94	604.04	639.97	1004.54

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

4. The 5 projects with maximum cost overruns in absolute term are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM COST OVERRUNS (as on 30-04-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹ ; crore)		
				COST ORIGINAL	COST ANTICIPATED	COST OVERRUN
1	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	2500.00	20000.00	17500.00
2	BANGALORE METRO RAIL PROJECT	Urban Development	05/2006	6395.00	11609.00	5214.00
3	SUBANSIRI LOWER H.E.P (NHPC)	Power	09/2003	6285.33	10667.00	4381.67
4	KUDANKULAM APP (NPCIL)	Atomic Energy	12/2001	13171.00	17270.00	4099.00
5	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR	Railways	09/1997	1000.00	4996.65	3996.65

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

5. Out of the 566 projects, 2 projects are ahead of schedule, 162 are on schedule and 261 are delayed with respect to latest schedule. However, the numbers of delayed projects further increases to 273 if delay is calculated on the basis of original schedule of completion. Further, 17 projects have been sanctioned without any commissioning schedule/date and for 124 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 261 delayed projects, 64 projects have overall delay in the range of 1 to 12 months, 64 projects have a delay in the range of 13 to 24 months, 77 projects have a delay in the range of 25 to 60 months and 56 projects have a delay of 61 months and above. The 5 projects with the maximum delay are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM TIME OVERRUNS (as on 30-04-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	DATE OF COMMISSIONING		TIME OVERRUNS (in months)
				ORIGINAL	ANTICIPATED	
1	GUNA-ETAWAH VIA SHIVPURI- GWALIOR - BHIND NL, (NCR)	Railways	04/1986	03/1994	10/2013	235
2	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	Railways	03/1984	03/1995	03/2013	216
3	UDHAMPUR- SRINAGAR- BARAMULLA (NL),NR	Railways	03/1995	03/2001	12/2017	201
4	BANKURA - DAMODAR (GC) (SER)	Railways	03/1998	03/2005	06/2016	135
5	LANJHIGARH- JUNAGARH NL(ECOR)	Railways	04/1993	03/2002	03/2013	132

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further time overruns.

6. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in forest clearance, contractual issue, delay in award of works, court cases, fund constraint, delay in re-prioritization of location, geological surprises, change in business process, ROU/ROW problems, law and order, etc.

7. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones drawn from the PERT Charts of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The earliest initiated 5 projects in which project agencies are not providing milestones are as below:-

List of 5 Earliest Projects without Milestones (as on 30-04-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹ crore)		EXPENDITURE CUMULATIVE (₹ crore)	DATE OF COMMISSIONING		MILESTONES
				ORIGINAL	ANTICIPATED		ORIGINAL	ANTICIPATED	
1	HOWRAH-AMTA-CHAMPADAN GA NL (SER)	Railways	04/1974	31.42	535.40	176.52	03/2007	03/2015	N.R.
2	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	37.68	1036.78	353.41	07/2012	N.R.	N.R.
3	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING	Railways	04/1983	36.80	703.17	247.74	N.R.	03/2015	N.R.
4	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	Railways	03/1984	520.00	634.13	555.27	03/1995	03/2013	N.R.
5	TAMLUK DIGHA,LINE DOUBLING (SER)	Railways	03/1984	293.97	1074.47	433.89	06/2005	06/2016	N.R.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up milestones.

N.R.: Not Reported.

8. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The earliest initiated 5 projects in which project agencies are not reporting/providing revised cost estimates are as below:-

List of 5 Earliest Projects without Revised Cost Estimates (as on 30-04-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹; crore)		EXPENDITURE CUMMULATIVE (₹; crore)
				ORIGINAL	REVISED	
1	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	04/1993	100.00	142.98	211.19
2	AMRAVATI-NARKHER NL(CR)	Railways	06/1994	120.90	284.27	541.95
3	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	12/1994	124.43	495.68	597.99
4	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	2500.00	2500.00	8549.43
5	KOTTUR-HARIHAR(NL),(SWR)	Railways	04/1995	65.94	302.23	344.29

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised cost estimates.

The earliest initiated 5 projects in which project agencies are not reporting/providing revised commissioning schedules are as below:-

List of 5 Earliest Projects without Revised Commissioning Schedule (as on 30.04.2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	DATE OF COMMISSIONING		
				ORIGINAL	REVISED	ANTICIPATED
1	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	07/2012	N.R.	N.R.
2	VIRAMGAM-BHILDI(WR),GC	Railways	04/1990	N.R.	03/2010	N.R.
3	AMRAVATI-NARKHER NL(CR)	Railways	06/1994	06/1999	03/2011	03/2011
4	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	12/1994	N.R.	N.R.	03/2012
5	KOTTUR-HARIHAR(NL),(SWR)	Railways	04/1995	N.R.	N.R.	12/2012

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised commissioning schedule.

N.R.: Not Reported.

9. **The Sector-wise details of delays/additional delays are as under:-**

i) In the **Steel Sector**, out of 17 projects, 13 projects are delayed. During the month project 'Bailadila Iron Ore Project Deposit- 11B, NMDC' has reported additional delays of 6 months. However, no specific reasons have been reported by the project authorities for delay in this project.

ii) In the **Coal Sector**, out of 52 projects, 29 projects are delayed. During the month 2 projects have reported additional delays of 4 and 12 months respectively, out of which 1 is a Mega project. The projects 'Krishnashila (4MTY), NCL' has reported additional delay of 12 months each due to delay in forest clearance. The project 'Neyveli New Thermal Power Project (2x500 MW), NLC' has reported additional delay of 4 months. However, no specific reasons have been reported by the project authorities for delay in this project.

iii) In the **Telecommunication Sector**, out of 13 projects, 5 projects are delayed. During the month 4 projects have reported additional delays in the range of 2-3 months. The projects 'GSM Equipment of 283000 Lines (2G) and 75000 Lines, BSNL' and 'Assam Telecom Circle, Phase-V.I, 2G & 3G, BSNL' have reported additional delay of 2 months each due to adverse weather condition and delay in permission to lay fiber cable from local bodies respectively. The Project 'ERP Implementation in BSNL on Turnkey basis, BSNL' has reported additional delay of 3 months due to change of business process and various issues related to vendor. The project 'Supply Installation Testing and Commissioning of Rural Wimax, BSNL' has reported additional delay of 2 months. However, no specific reasons have been reported by the project authorities for delay in this project.

iv) In the **Shipping & Ports Sector**, out of 19 projects, 2 projects are delayed. During the month 5 projects have reported additional delays in the range of 1-10 months, out of which 2 projects are Mega projects. Of these 5 projects, 2 projects have reported additional delay of 1 and 2 months respectively; the projects 'Setting up of LNG Regasification Terminal at Puthu, Port Trust', 'Acquisition of Six (6) Nos. of Anchor Handling Tug Cum Supply, Shipping Corporation of India' and 'Acquisition of 4 Nos. of Anchor Handling Cum Supply, Shipping Corporation of India' have reported additional delay of 3, 5 and 10 months respectively. However, no specific reasons have been reported by the project authorities for delay in these projects.

v) In the **Railways Sector**, out of 129 projects, 31 projects are delayed. During the

month 5 projects have reported additional delays in the range of 1-24 months, out of which 2 are Mega projects. Of these 5 projects, 2 projects have reported additional delay of 1 and 3 month respectively; the project 'Extension of MRTS from Velachery to Station Thomas, MTP, MRTP' has reported additional delay of 9 months due to contractual issue; the project 'Belapur-Seawood-Uran Electrified Double Line (MTP), MRTP' has reported additional delay of 24 months due to fund constraint. The project 'Mumbai Urban Transport Project Phase-II, MRTP' has reported additional delay of 9 months. However, no specific reasons have been reported by the project authorities for delay in this project.

vi) In the **Petroleum Sector**, out of 70 projects, 38 projects are delayed. During the month 7 projects have reported additional delays in the range of 1-2 months, out of which 5 are Mega projects. Of these 7 projects, 2 projects have reported additional delay of 1 month each; the projects 'Development of C-Series Fields, ONGC' and 'Development of B-22 Cluster Fields, ONGC' have reported additional delay of 2 month each due to delay I re-prioritization of location and court cases respectively; the projects 'Butadiene Extraction Unit (BDEU) at PANIPA, IOCL' and 'Development of BHE and BH-35 Area, ONGC' have reported additional delay of 2 months each due to contractual issue and delay in award of works respectively. The project 'Hydrocracker Revamp and Setting up a New CCR at Mumbai, BPCL' has reported additional delay of 2 months. However, no specific reasons have been reported by the project authorities for delay in this project.

vii) In the **Power Sector**, out of 100 projects, 51 projects are delayed. During the month 16 projects have reported additional delays in the range of 1-13 months, out of which 9 are Mega projects. Of these 16 projects, 2 projects have reported additional delay of 1 month each, 2 project has reported additional delay of 2 months, 5 projects have reported additional delay of 3 months each and 2 projects have reported additional delay of 4 months each; the projects 'Transmission System for Transfer of Power from Generation, PGCIL' and 'Eastern Region Transmission System-III, PGCIL' have reported additional delay of 6 months each due to delay in land acquisition. The projects 'Transmission System for Phase-1 Generation Project, PGCIL' and 'Transmission System for Transfer of Power from Generation-Part B, PGCIL' have reported additional delay of 10 and 13 months respectively due to delay in land acquisition. The project 'Transmission System of Vindhyachal-IV and Rihand-I, PGCIL' has reported additional delay of 12 months due to delay in forest clearance.

viii) In the **Road Transport & Highways Sector**, out of 149 projects, 88 are delayed. During the month 13 projects have reported additional delays in the range of 1-18 months. Of these 13 projects, 6 projects have reported additional delay of 1 month each and 4

projects have reported additional delay of 2 months each; the projects 'Trichy - Korur NH-67, NHAI' and 'Ganga Bridge to Ramdevi Crossing PH.II NH-25, KM.75-80.06, NHAI' have reported additional delay of 6 and 12 months respectively. The project 'Dindigul – Kumli, NHAI' has reported additional delay of 18 months. The project implementing agency has not mentioned any specific reasons for delay in these projects. However, general reasons for delay in these projects are delay in land acquisition, delay in forest & environment clearance, utility shifting problem, poor performance of contractor, etc.

10. The status as on 30.04.2013 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

11. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	Road Transport & Highways	149	13
2	Railways	129	5
3	Power	100	16
4	Petroleum	70	7
5	Coal	52	2
6	Shipping & Ports	19	5
7	Steel	17	1
8	Telecommunications	13	4
9	Civil Aviation	6	0
10	Atomic Energy	4	0
11	Urban Development	4	0
12	Fertilisers	1	0
13	Petrochemicals	1	0
14	Water Resources	1	0
	Total	566	53

Month wise List of Completed Project Costing Rs. 150 Crore and above during
2013-2014

Sl. No.	Project Name	Original Cost (Rs. crore)	Original Date Of commissi oning	Cumulative Expenditure (Rs. crore)
April, 2013				
<u>Power</u>				
1	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000091]	209.78	08/2013	52.2
<u>Railways</u>				
2	REINGUNTA-GUNTAKAL(RE)(RAIL VIKAS NIGAM LTD.) - [220100260]	168.34	04/2003	343.36
3	BILASPUR-URKURA (DL)(RAIL VIKAS NIGAM LTD.) - [220100321]	151.52	-	315


Summary of projects in the Flash Report for the month of April, 2013

I. Project Implementation - Current Status:

Number of Projects in Previous Month	558
Number of Projects completed/dropped/frozen in Current Month	3
Number of Projects Added in Current Month	11
Number of Projects in Current Month	566


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 566 projects, 3 projects are ahead of schedule, 149 projects are on schedule and 273 projects are delayed. Of the balance, 124 projects do not have fixed dates of commissioning while 17 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

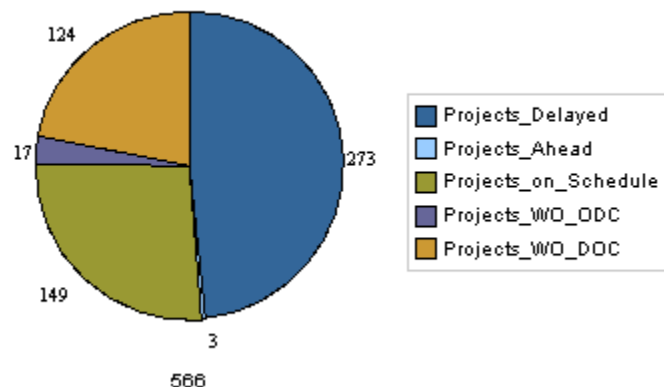

III. Investment Scenario

The Total Original cost of implementation of 566 projects when sanctioned, was of the order of Rs. 798047.83 crore but this was subsequently revised to Rs. 943167.88 crore implying a cost overrun of 18.2%. The expenditure incurred on these projects till April, 2013 is Rs. 456277.05 crore, which is 48.4% of the revised cost of the projects.

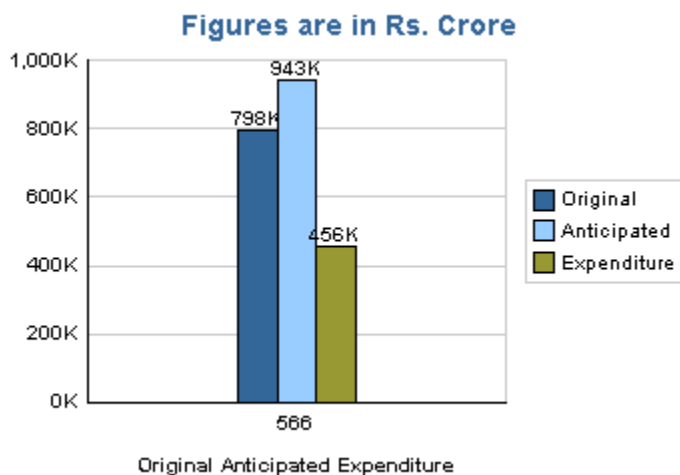

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	558
No of Projects Completed/Dropped/Frozen in Current Month	3
No of Projects added in Current Month	11
No of Projects in Current Month	566

II. Project status

With Respect To	Number of Projects					Total	Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C		
Original (Date)	273	3	149	17	124	566	48.23
Latest Approved (Date)	261	2	162	17	124	566	46.11

III. (A) Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	421	675,483.09	714,599.25	325,289.25	45.50	39,116.16	5.80
Latest Approved (RCE)	145	177,690.78	228,568.63	130,987.80	57.30	50,877.85	28.60
Total (RCE)	566	853,173.87	943,167.88	456,277.05	48.38	89994.01	10.55
Original Cost of All Projects							
Original Cost	566	798,047.83	943,167.88	456,277.05	48.40	145,120.05	18.20

III. (B) Delayed Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	273	436,822.20	525,231.96	317,772.13	60.50	88,409.76	20.20
Latest Approved (RCE)	261	453,464.23	508,848.55	309,206.50	60.80	55,384.32	12.20

IV. Additional Delayed Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Latest Approved	53	71,333.11	79,386.94	47,835.77	60.30	8,053.83	11.30

Extent of cost overruns in projects with respect to original schedule(Sector Wise)

S.N.	Sector	No. of Projects	Total cost (Rs. crore.)			Projects with cost overrun			
			Original	Anticipated cost	Cost overrun (%)	No .	Original Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cost Overrun (%)
1	Atomic Energy	4	40,442.0	46,726.0	15.5	2	16,663.0	22,947.0	37.7
2	Civil Aviation	6	5,473.6	6,063.1	10.8	2	3,750.5	4,340.0	15.7
3	Coal	52	36,486.6	37,940.7	4.0	7	8,579.5	10,631.3	23.9
4	Fertilisers	1	1,478.6	1,478.6	0.0	0	0.0	0.0	0.0
5	Steel	17	65,285.9	71,443.4	9.4	6	24,028.9	30,216.4	25.8
6	Petrochemicals	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	63.4
7	Petroleum	70	165,950.5	178,609.9	7.6	18	54,882.5	74,497.3	35.7
8	Power	100	242,845.0	258,586.3	6.5	18	45,722.0	61,463.3	34.4
9	Railways	129	66,990.8	155,817.8	132.6	108	38,966.0	127,839.6	228.1
10	Road Transport & Highways	149	101,529.8	103,468.4	1.9	11	3,324.3	5,445.2	63.8
11	Shipping & Ports	19	15,617.1	17,902.4	14.6	9	8,629.0	11,218.5	30.0
12	Telecommunications	13	5,699.2	5,506.3	-3.4	2	477.3	550.9	15.4
13	Urban Development	4	44,245.2	49,518.1	11.9	2	6,509.2	11,782.1	81.0
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		566	798,047.8	943,167.9	18.2	187	217,535.5	371,038.5	70.6

Extent of cost overruns in projects with respect to original schedule(State Wise)

S.N	State	No. of Proj- ects	Total cost (Rs. crore)			Projects with cost overrun			
			Original	Anticipated Cost	Cost overrun (%)	No.	Original Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cost overrun (%)
1	Andhra Pradesh	34	28,405.6	36,261.8	27.7	14	12,923.7	21,646.9	67.5
2	Arunachal Pradesh	4	9,512.2	14,144.3	48.7	2	6,441.3	11,073.4	71.9
3	Assam	34	22,035.9	35,386.1	60.6	12	10,491.8	23,936.0	128.1
4	Bihar	30	26,917.6	35,131.2	30.5	15	12,886.5	21,100.1	63.7
5	Goa	1	335.6	335.6	0.0	0	0.0	0.0	0.0
6	Gujarat	22	33,405.1	33,607.0	0.6	5	2,413.7	2,885.5	19.5
7	Haryana	8	4,054.4	5,737.0	41.5	2	1,298.8	2,981.4	129.5
8	Himachal Pradesh	5	13,355.6	17,246.7	29.1	4	11,308.5	15,199.7	34.4
9	Jammu and Kashmir	10	14,927.0	34,825.6	133.3	6	7,866.5	27,765.1	253.0
10	Karnataka	27	47,076.4	56,526.2	20.1	10	9,330.8	19,187.1	105.6
11	Kerala	7	20,376.7	21,818.2	7.1	3	4,295.7	5,737.2	33.6
12	Madhya pradesh	20	18,545.6	18,939.9	2.1	3	1,798.1	2,611.8	45.3
13	Maharashtra	48	88,574.5	100,147.9	13.1	15	27,055.5	41,095.8	51.9
14	Manipur	1	727.6	4,453.5	512.1	1	727.6	4,453.5	512.1
15	Meghalaya	2	762.0	762.0	0.0	0	0.0	0.0	0.0
16	Mizoram	2	1,533.0	3,298.0	115.1	1	619.3	2,384.3	285.0
17	Nagaland	1	850.0	2,446.8	187.9	1	850.0	2,446.8	187.9
18	Odisha	30	56,171.6	63,436.9	12.9	12	32,671.6	39,936.9	22.2
19	Punjab	6	3,542.0	4,483.8	26.6	2	532.4	1,474.2	176.9
20	Rajasthan	14	21,115.8	20,928.0	-0.9	3	1,080.0	1,344.9	24.5
21	Sikkim	2	1,648.9	3,690.0	123.8	1	1,339.5	3,380.6	152.4
22	Tamil Nadu	32	48,788.1	60,101.4	23.2	14	29,143.5	40,456.9	38.8
23	Tripura	3	1,522.4	2,018.9	32.6	2	1,234.4	1,765.2	43.0
24	Uttar Pradesh	28	21,622.6	25,904.7	19.8	10	3,831.0	8,161.4	113.0
25	West Bengal	27	46,938.9	59,049.3	25.8	15	20,928.4	33,038.8	57.9
26	Delhi	4	38,214.4	38,194.8	-0.1	0	0.0	0.0	0.0
27	Chhatisgarh	24	58,278.3	59,362.9	1.9	5	1,396.8	2,481.4	77.6
28	Jharkhand	23	14,447.4	18,650.8	29.1	7	2,225.5	6,600.7	196.6
29	Uttarakhand	5	7,624.2	8,564.6	12.3	2	2,640.7	3,581.2	35.6
30	Multi State	112	146,738.7	157,714.0	7.5	20	10,203.9	24,312.0	138.3
Total		566	798,047.8	943,167.9	18.2	187	217,535.5	371,038.5	70.6

Extent of the time overruns in projects with respect to original schedule

S. No	Sector	No. of Projects	Total cost (Rs. crore)			Projects with time overruns			
			Original	Anticipated cost	Cost overrun (%)	No.	Original Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Range (in Months)
1	Atomic Energy	4	40,442.0	46,726.0	15.5	2	23,779.0	23,779.0	3 - 11
2	Civil Aviation	6	5,473.6	6,063.1	10.8	2	645.1	645.1	13 - 35
3	Coal	52	36,486.6	37,940.7	4.0	29	25,052.8	26,878.2	12 - 72
4	Fertilisers	1	1,478.6	1,478.6	0.0	0	0.0	0.0	-
5	Steel	17	65,285.9	71,443.4	9.4	15	64,698.3	70,855.9	4 - 44
6	Petrochemicals	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	20 - 20
7	Petroleum	70	165,950.5	178,609.9	7.6	40	110,593.6	125,191.6	1 - 120
8	Power	100	242,845.0	258,586.3	6.5	51	124,167.7	138,072.8	1 - 102
9	Railways	129	66,990.8	155,817.8	132.6	33	24,276.3	69,751.0	3 - 235
10	Road Transport & Highways	149	101,529.8	103,468.4	1.9	88	48,631.5	50,543.3	2 - 111
11	Shipping & Ports	19	15,617.1	17,902.4	14.6	7	6,582.5	7,834.6	5 - 87
12	Telecommunications	13	5,699.2	5,506.3	-3.4	5	2,934.9	2,760.6	27 - 55
13	Urban Development	4	44,245.2	49,518.1	11.9	0	0.0	0.0	-
14	Water Resources	1	542.9	1,187.0	118.6	0	0.0	0.0	-
Total		566	798,047.8	943,167.9	18.2	273	436,822.2	525,232.0	

Extent of the time overruns in projects with respect to original schedule(State Wise)

S. No	State	No. of Projects	Total cost (Rs. crore)			Projects with time overruns			
			Original	Anticipated cost	Cost overrun (%)	No.	Original Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Range (in Months)
1	Andhra Pradesh	34	28,405.6	36,261.8	27.7	13	17,373.0	21,548.4	4 - 44
2	Arunachal Pradesh	4	9,512.2	14,144.3	48.7	3	9,356.2	13,737.9	25 - 87
3	Assam	34	22,035.9	35,386.1	60.6	31	20,716.4	33,237.3	12 - 120
4	Bihar	30	26,917.6	35,131.2	30.5	11	20,239.3	24,919.6	2 - 98
5	Goa	1	335.6	335.6	0.0	1	335.6	335.6	13 - 13
6	Gujarat	22	33,405.1	33,607.0	0.6	5	15,029.6	14,968.3	9 - 15
7	Haryana	8	4,054.4	5,737.0	41.5	4	2,216.6	3,396.6	4 - 50
8	Himachal Pradesh	5	13,355.6	17,246.7	29.1	5	13,355.6	17,246.7	26 - 102
9	Jammu and Kashmir	10	14,927.0	34,825.6	133.3	7	13,038.7	32,618.8	10 - 201
10	Karnataka	27	47,076.4	56,526.2	20.1	10	18,014.8	18,104.0	6 - 106
11	Kerala	7	20,376.7	21,818.2	7.1	5	19,581.0	20,231.0	5 - 58
12	Madhya pradesh	20	18,545.6	18,939.9	2.1	9	3,620.0	3,732.8	9 - 69
13	Maharashtra	48	88,574.5	100,147.9	13.1	25	44,540.5	51,105.5	2 - 144
14	Manipur	1	727.6	4,453.5	512.1	1	727.6	4,453.5	72 - 72
15	Meghalaya	2	762.0	762.0	0.0	0	0.0	0.0	-
16	Mizoram	2	1,533.0	3,298.0	115.1	2	1,533.0	3,298.0	7 - 35
17	Nagaland	1	850.0	2,446.8	187.9	1	850.0	2,446.8	24 - 24
18	Odisha	30	56,171.6	63,436.9	12.9	16	49,397.9	52,739.8	3 - 136
19	Punjab	6	3,542.0	4,483.8	26.6	2	989.0	1,064.0	7 - 64
20	Rajasthan	14	21,115.8	20,928.0	-0.9	7	15,830.9	15,384.6	3 - 59
21	Sikkim	2	1,648.9	3,690.0	123.8	2	1,648.9	3,690.0	15 - 35
22	Tamil Nadu	32	48,788.1	60,101.4	23.2	11	16,915.5	18,367.4	5 - 87
23	Tripura	3	1,522.4	2,018.9	32.6	2	1,101.4	1,395.4	10 - 21
24	Uttar Pradesh	28	21,622.6	25,904.7	19.8	14	12,466.3	14,914.0	8 - 84
25	West Bengal	27	46,938.9	59,049.3	25.8	12	22,920.5	29,479.3	3 - 141
26	Delhi	4	38,214.4	38,194.8	-0.1	0	0.0	0.0	-
27	Chhatisgarh	24	58,278.3	59,362.9	1.9	9	23,484.9	23,796.2	12 - 59
28	Jharkhand	23	14,447.4	18,650.8	29.1	10	9,422.6	9,529.2	5 - 60
29	Uttarakhand	5	7,624.2	8,564.6	12.3	4	6,097.2	7,037.6	5 - 50
30	Multi State	112	146,738.7	157,714.0	7.5	51	76,019.2	82,453.7	1 - 235
Total		566	798,047.8	943,167.9	18.2	273	436,822.2	525,232.0	

Extent of the time overruns in projects with respect to latest schedule

S. No	Sector	No. of Projects	Total cost (Rs. crore)			Projects with time overruns			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost (Rs. crore)	Anticipated Cost (Rs. crore)	Range (in Months)
1	Atomic Energy	4	40,442.0	46,726.0	15.5	2	23,779.0	23,779.0	3 - 11
2	Civil Aviation	6	5,473.6	6,063.1	10.8	2	645.1	645.1	13 - 35
3	Coal	52	36,486.6	37,940.7	4.0	29	25,052.8	26,878.2	12 - 72
4	Fertilisers	1	1,478.6	1,478.6	0.0	0	0.0	0.0	-
5	Steel	17	65,285.9	71,443.4	9.4	13	63,227.8	69,385.3	4 - 44
6	Petrochemicals	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
7	Petroleum	70	165,950.5	178,609.9	7.6	38	109,858.4	122,853.8	1 - 87
8	Power	100	242,845.0	258,586.3	6.5	51	124,167.7	138,072.8	1 - 102
9	Railways	129	66,990.8	155,817.8	132.6	31	23,761.3	68,320.6	3 - 235
10	Road Transport & Highways	149	101,529.8	103,468.4	1.9	88	48,631.5	50,543.3	2 - 111
11	Shipping & Ports	19	15,617.1	17,902.4	14.6	2	4,728.0	5,610.0	18 - 40
12	Telecommunications	13	5,699.2	5,506.3	-3.4	5	2,934.9	2,760.6	27 - 55
13	Urban Development	4	44,245.2	49,518.1	11.9	0	0.0	0.0	-
14	Water Resources	1	542.9	1,187.0	118.6	0	0.0	0.0	-
Total		566	798,047.8	943,167.9	18.2	261	426,786.4	508,848.6	

Extent of cost overruns in projects with respect to latest schedule

S.No.	Sector	No. of projects	Total cost (Rs. crore)			Projects with cost overruns			
			Latest approved	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost (Rs crore)	Anticipated Cost (Rs crore)	Cost overrun (%)
1	Atomic Energy	4	40,442.0	46,726.0	15.5	2	16,663.0	22,947.0	37.7
2	Civil Aviation	6	5,680.6	6,063.1	6.7	1	1,942.5	2,325.0	19.7
3	Coal	52	37,452.6	37,940.7	1.3	6	7,115.6	7,603.7	6.9
4	Fertilisers	1	1,478.6	1,478.6	0.0	0	0.0	0.0	0.0
5	Steel	17	67,562.2	71,443.4	5.7	4	9,290.0	13,201.3	42.1
6	Petrochemicals	1	8,920.0	8,920.0	0.0	0	0.0	0.0	0.0
7	Petroleum	70	179,674.1	178,609.9	-0.6	2	30,602.0	34,537.0	12.9
8	Power	100	246,360.7	258,586.3	5.0	14	39,450.6	51,676.2	31.0
9	Railways	129	95,971.2	155,817.8	62.4	79	43,299.0	103,177.3	138.3
10	Road Transport & Highways	149	101,696.3	103,468.4	1.7	11	3,324.3	5,445.2	63.8
11	Shipping & Ports	19	17,389.4	17,902.4	3.0	6	3,312.5	4,036.9	21.9
12	Telecommunications	13	5,699.2	5,506.3	-3.4	2	477.3	550.9	15.4
13	Urban Development	4	44,304.1	49,518.1	11.8	1	6,395.0	11,609.0	81.5
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		566	853,173.9	943,167.9	10.5	129	162,414.6	258,296.4	59.0

Extent of time & cost overruns in projects with respect to latest schedule

S No.	Sector	No. of projects	Total Cost (Rs. crore)			Projects with time & cost overruns			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original Cost (Rs. crore)	Anticipated Cost (Rs crore)	Range (in Months)
1	Atomic Energy	4	40,442.00	46,726.00	15.54	0	0.00	0.00	0- 0
2	Civil Aviation	6	5,473.58	6,063.07	10.77	1	1,808.00	2,015.00	13- 13
3	Coal	52	36,486.60	37,940.66	3.99	0	0.00	0.00	0- 0
4	Fertilisers	1	1,478.63	1,478.63	0.00	0	0.00	0.00	0- 0
5	Steel	17	65,285.87	71,443.41	9.43	1	295.89	607.17	24- 24
6	Petrochemicals	1	5,460.61	8,920.00	63.35	1	5,460.61	8,920.00	20- 20
7	Petroleum	70	165,950.52	178,609.86	7.63	11	21,026.22	34,896.99	13- 120
8	Power	100	242,845.00	258,586.29	6.48	2	2,253.45	3,986.02	0- 76
9	Railways	129	66,990.82	155,817.76	132.60	17	6,331.52	23,220.15	0- 144
10	Road Transport & Highways	149	101,529.76	103,468.38	1.91	0	0.00	0.00	0- 0
11	Shipping & Ports	19	15,617.12	17,902.42	14.63	5	5,400.70	6,860.25	10- 87
12	Telecommunications	13	5,699.24	5,506.32	-3.39	0	0.00	0.00	0- 0
13	Urban Development	4	44,245.18	49,518.08	11.92	0	0.00	0.00	0- 0
14	Water Resources	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		566	798047.83	943167.88	18.18	38	42576.39	80505.58	

Extent of time & cost overruns in projects with respect to original schedule

S No.	Sector	No. of projects	Total Cost (Rs. crore)			Projects with time & cost overruns			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Range (in Months)
1	Atomic Energy	4	40,442.00	46,726.00	15.54	0	0.00	0.00	0- 0
2	Civil Aviation	6	5,473.58	6,063.07	10.77	0	0.00	0.00	0- 0
3	Coal	52	36,486.60	37,940.66	3.99	5	7,938.86	9,942.56	16- 55
4	Fertilisers	1	1,478.63	1,478.63	0.00	0	0.00	0.00	0- 0
5	Steel	17	65,285.87	71,443.41	9.43	6	24,028.89	30,216.43	8- 44
6	Petrochemicals	1	5,460.61	8,920.00	63.35	1	5,460.61	8,920.00	20- 20
7	Petroleum	70	165,950.52	178,609.86	7.63	15	51,842.82	70,539.61	2- 120
8	Power	100	242,845.00	258,586.29	6.48	13	36,844.69	50,749.71	10- 102
9	Railways	129	66,990.82	155,817.76	132.60	28	15,647.41	61,126.99	12- 235
10	Road Transport & Highways	149	101,529.76	103,468.38	1.91	10	3,158.01	5,252.10	21- 109
11	Shipping & Ports	19	15,617.12	17,902.42	14.63	3	4,878.00	6,210.00	18- 87
12	Telecommunications	13	5,699.24	5,506.32	-3.39	1	149.15	158.72	50- 50
13	Urban Development	4	44,245.18	49,518.08	11.92	0	0.00	0.00	0- 0
14	Water Resources	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		566	798047.83	943167.88	18.18	82	149948.44	243116.12	

V. List of projects completed/dropped/Frozen current month

(All Cost
/Expenditure
in Rs. crore)

S.no	Project	DOA	Original		Now anticipated		Final
			Cost	DOC	Cost	DOC	Expenditure
<u>Power</u>							
1	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII	12/2010	209.78	08/2013	209.78	03/2013	52.20
<u>Railways</u>							
2	REINGUNTA-GUNTAKAL(RE)	06/2000	168.34	04/2003	370.00	N.A.	343.36
3	BILASPUR-URKURA (DL)	04/1997	151.52	N.A.	350.00	N.A.	315.00

VI. List of projects added

(All Cost in Rs. crore)

S.no	Project	Original		Anticipated		DOC
		DOA	Cost	DOC	Cost	
<u>Coal</u>						
1	RFR OF MANUGURU OC PROJECT	11/2012	430.14	/	430.14	-
<u>Petroleum</u>						
2	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	11/2012	309.81	8/2014	309.81	8/2014
3	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG	1/2006	672.00	10/2011	1,038.00	12/2013
4	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	1/2006	732.00	10/2011	1,227.00	12/2013
<u>Railways</u>						
5	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP	3/2013	307.00	/	307.00	-
6	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP	3/2007	243.78	/	243.78	-
7	BHOJIPUR TANAKPUR VIA PILIBHIT	3/2008	195.64	/	195.64	-
8	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP	3/2012	160.89	/	199.75	-
9	CHHAPRA-BALLIA UP	3/2013	295.00	/	295.00	-
10	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	3/2013	4,874.58	3/2016	4,874.58	3/2016
11	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP	3/2013	643.00	/	643.00	-

VII. Milestones (Cumulative due & achieved)

Total	3446
Achieved up to month	1272

VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>Coal</u>						
1	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) NLC	5,907.11	5,907.11	12/2015	08/2017	12/2017	4
2	KRISHNASHILA (NCL) (4MTY) NCL	789.88	741.62	03/2013	03/2013	03/2014	12
	<u>Steel</u>						
3	Bailadila Iron Ore Project Deposit- 11B (NMDC) NMDC	295.89	607.17	12/2011	06/2013	12/2013	6
	<u>Petroleum</u>						
4	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 ONGC	5,713.03	8,813.41	05/2010	05/2013	06/2013	1
5	Fluidized catalytic cracking unit(FCCU) revamp IOCL	1,000.00	1,000.00	01/2013	08/2013	09/2013	1
6	DEVELOPMENT OF C-SERIES FIELDS ONGC	3,195.16	3,690.37	12/2008	04/2013	06/2013	2
7	DEVELOPMENT OF B-22 CLUSTER FIELDS ONGC	2,323.40	2,920.82	09/2010	04/2013	06/2013	2
8	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MU BPCL	825.00	1,827.00	04/2013	04/2013	06/2013	2
9	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT IOCL	341.50	341.50	02/2013	04/2013	06/2013	2
10	Development of BHE and BH-35 Area. ONGC	372.11	372.11	03/2013	04/2013	06/2013	2
	<u>Power</u>						
11	RAMPUR HEP(412 MW) SJVNL	2,047.03	2,047.03	01/2012	02/2014	03/2014	1
12	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B PGCIL	160.32	160.32	10/2012	04/2013	05/2013	1
13	TEESTA LOW DAM HEP, STAGE-IV (NHPC) NHPC	1,061.38	1,501.75	09/2009	03/2014	05/2014	2
14	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP PGCIL	557.24	758.75	01/2010	04/2013	06/2013	2
15	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT PGCIL	11,130.19	11,130.19	08/2013	03/2015	06/2015	3
16	Trans. System associated with PALLATANA GBPP & BPT PGCIL	2,144.00	2,144.00	12/2012	12/2013	03/2014	3
17	System Strengthening in NR for SASAN & MUNDRA (UMPP) PGCIL	1,216.83	1,216.83	08/2012	03/2014	06/2014	3
18	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME PGCIL	965.58	965.58	11/2012	12/2013	03/2014	3
19	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI PGCIL	2,074.86	2,074.86	03/2013	12/2013	03/2014	3
20	NIMOO BAZGO HYDROELECTRIC PROJECT NHPC	611.01	936.00	08/2010	06/2013	10/2013	4


VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
21	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV PGCIL	520.48	520.48	11/2011	03/2014	07/2014	4
22	Transmission system for transfer of power from Gen. PGCIL	250.03	250.03	01/2013	06/2014	12/2014	6
23	EASTERN REGION TRANSMISSION SYSTEM-III PGCIL	1,272.80	1,272.80	11/2012	03/2014	09/2014	6
24	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECT PGCIL	558.26	558.26	11/2013	11/2013	09/2014	10
25	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I PGCIL	4,672.99	4,672.99	11/2012	03/2014	03/2015	12
26	Transmission system for transfer of power from Gen-PART B PGCIL	1,585.12	1,585.12	11/2013	11/2013	12/2014	13
Railways							
27	LANJHIGARH-JUNAGARH NL(ECOR) ECOR	100.00	227.94	03/2002	06/2013	07/2013	1
28	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA RE	171.10	246.44	03/2012	12/2013	03/2014	3
29	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP MRT	495.74	495.74	06/2013	03/2014	12/2014	9
30	MUMBAI URBAN TRANSPORT PROJECT PHASE-II MRT	5,300.00	5,300.00	03/2014	03/2016	12/2016	9
31	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) MRT	401.81	1,512.86	03/2004	03/2014	03/2016	24
Road Transport & Highways							
32	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) NHAI	225.00	241.53	04/2004	04/2013	05/2013	1
33	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 NHAI	340.68	340.68	03/2008	04/2013	05/2013	1
34	GANJAM-ICCHAPURUM,NH-5(NHAI) NHAI	263.27	263.27	02/2004	04/2013	05/2013	1
35	GWALIOR BYPASS, NH-75,3 NHAI	300.93	300.93	10/2009	04/2013	05/2013	1
36	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 NHAI	228.70	228.70	02/2004	04/2013	05/2013	1
37	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM NHAI	852.00	852.00	03/2013	07/2013	08/2013	1
38	NEW MANGALORE PORT NH-17 AND 48 NHAI	196.50	196.50	06/2011	04/2013	06/2013	2
39	THANJAUR-TRICHY,NH-67(NHAI) NHAI	280.00	280.00	06/2009	04/2013	06/2013	2
40	Jaipur-Tonk-Deoli NHAI	792.06	792.06	12/2012	04/2013	06/2013	2
41	Armur to kadloor yellareddy NHAI	390.56	390.56	02/2012	04/2013	06/2013	2
42	TRICHY - KORUR NH-67 NHAI	516.00	516.00	07/2010	09/2013	03/2014	6
43	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 NHAI	155.00	201.66	09/2008	03/2013	03/2014	12
44	Dindigul - Kumli NHAI	485.00	485.00	08/2013	08/2013	02/2015	18
Shipping & Ports							
45	Acquisition of three(3) nos of 6500TEU Cellular container SHIPP.	1,028.10	1,012.23	12/2013	10/2013	11/2013	1


VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
46	Setting up of Single Point Mooring (SPM) and allie PORT TRUST	830.00	621.53	05/2013	03/2013	05/2013	2
47	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU PORT TRUST	3,500.00	4,150.00	01/2012	04/2013	07/2013	3
48	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPL SHIPP.	511.87	511.87	03/2014	03/2014	08/2014	5
49	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY SHIPP.	359.44	359.44	04/2011	11/2012	09/2013	10
<u>Telecommunications</u>							
50	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES BSNL	149.15	158.72	06/2009	06/2013	08/2013	2
51	Assam Telecom Circle, Phase-V.I, 2G & 3G BSNL	336.81	336.81	01/2009	06/2013	08/2013	2
52	Supply Installation testing and commissioning of Rural Wimax BSNL	1,148.19	964.37	05/2011	06/2013	08/2013	2
53	ERP implementation in BSNL on Turnkey basis BSNL	384.00	384.00	10/2010	09/2013	12/2013	3

Graphical Analysis of All Projects w.r.t. Original Schedule

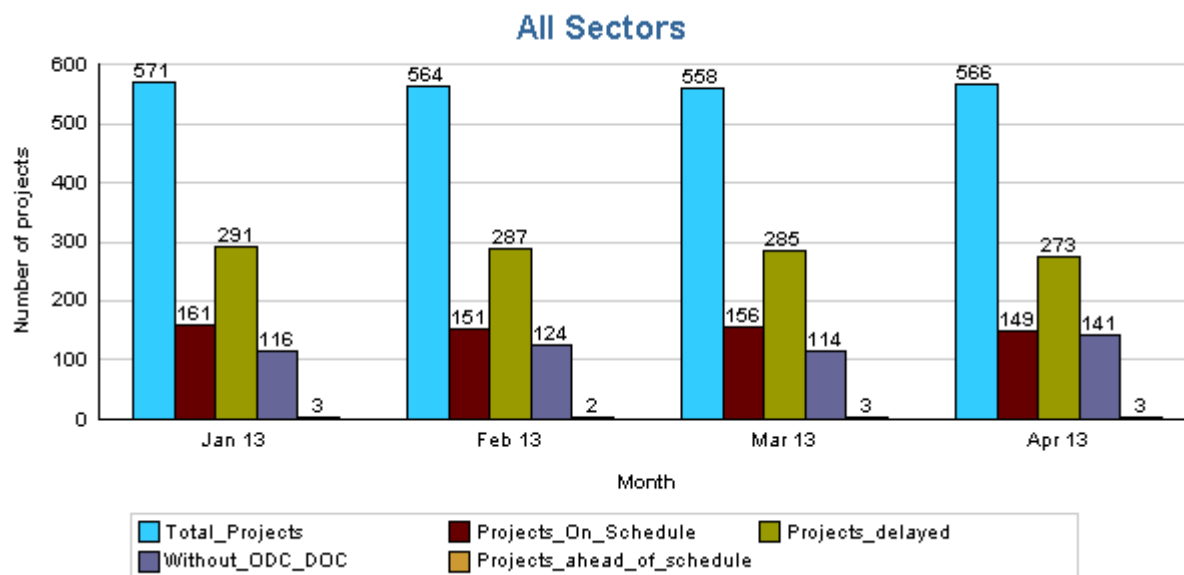


Break-up of 273 Delayed projects in April 2013

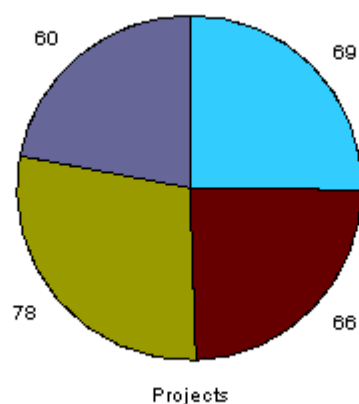


Delay in Months



Graphical Analysis of All Projects w.r.t. Revised Schedule

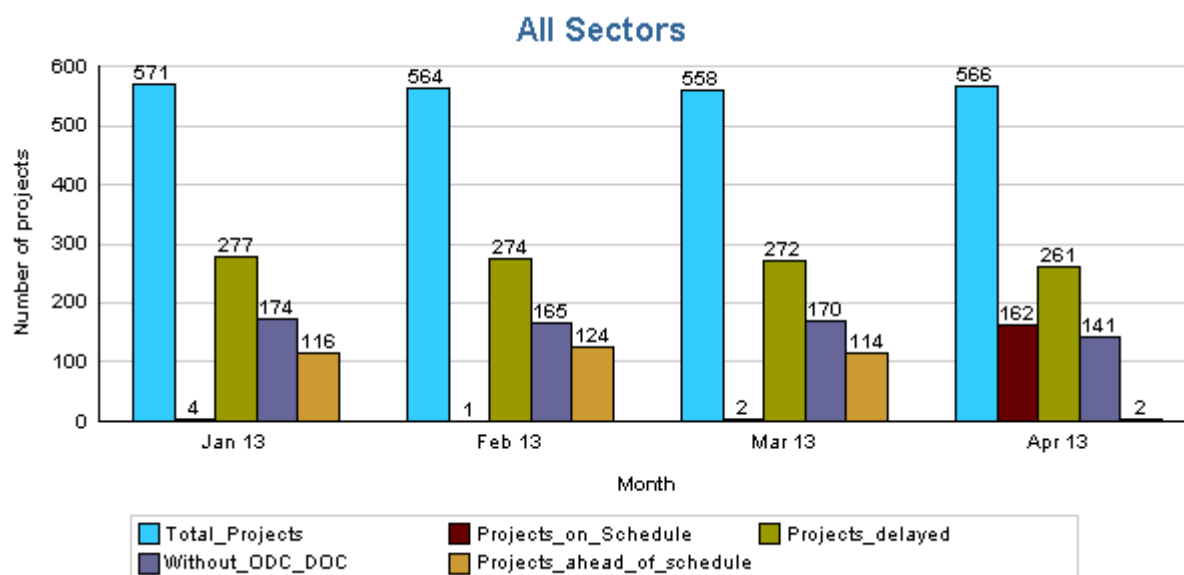


Break-up of 261 Delayed projects in April 2013

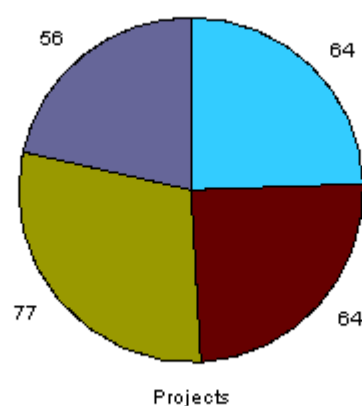

Delay in Months



Graphical Analysis of Urban Development Sector

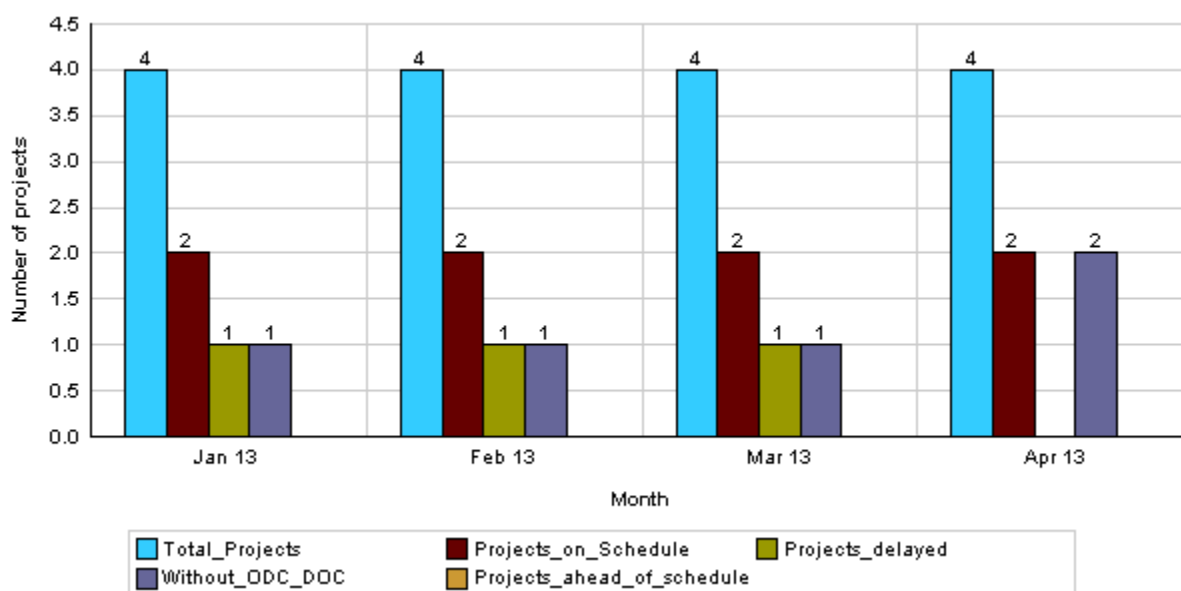


Break-up of 0 Delayed projects in April 2013


Delay in Months



Graphical Analysis of Telecommunications Sector

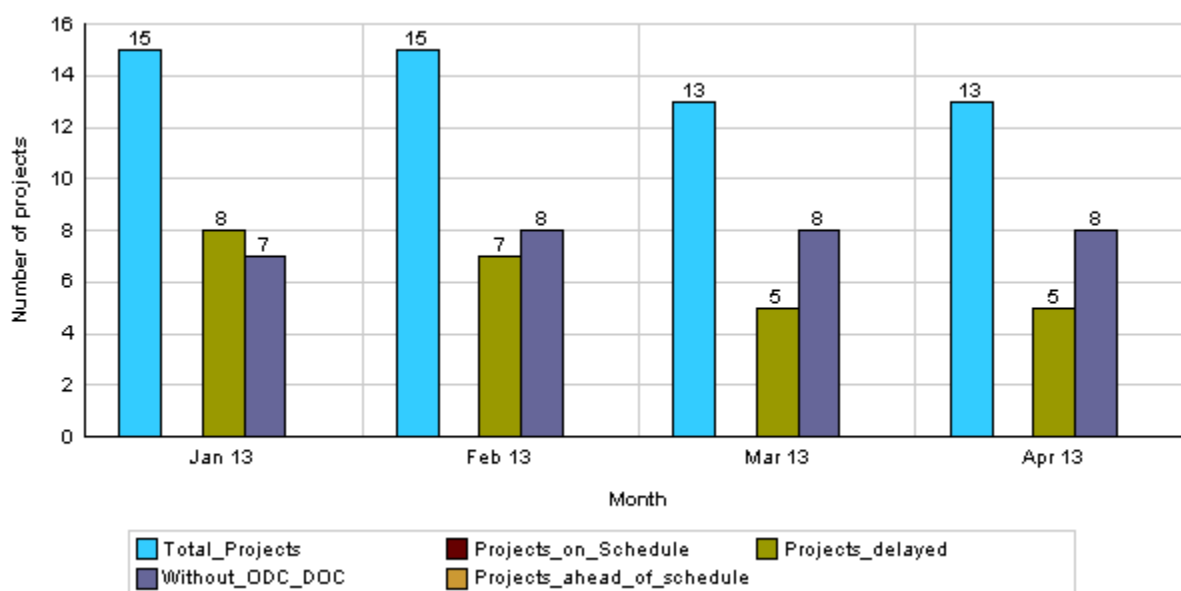


Break-up of 5 Delayed projects in April 2013

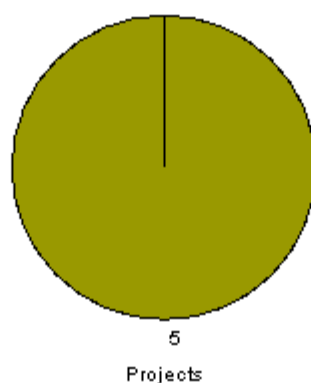


Delay in Months



Graphical Analysis of Shipping & Ports Sector

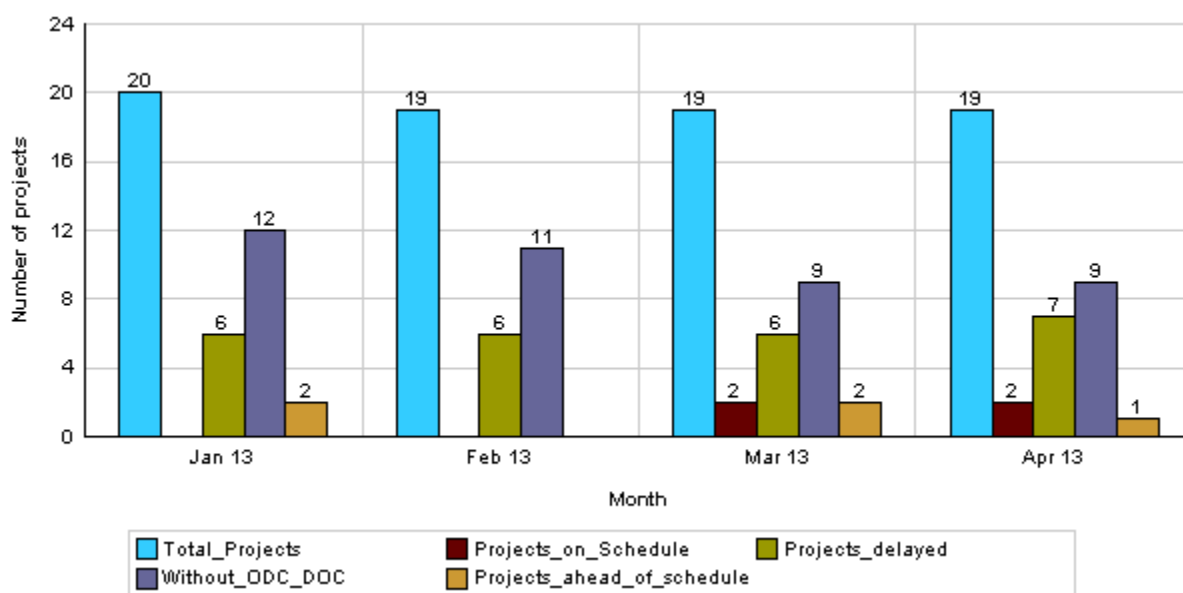


Break-up of 7 Delayed projects in April 2013

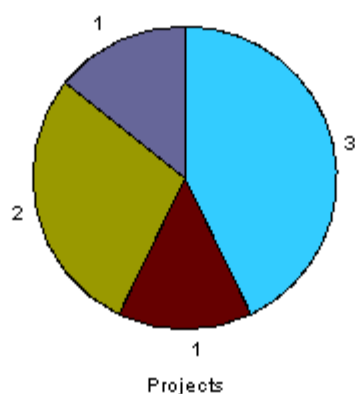


Delay in Months



Graphical Analysis of Road Transport & Highways Sector

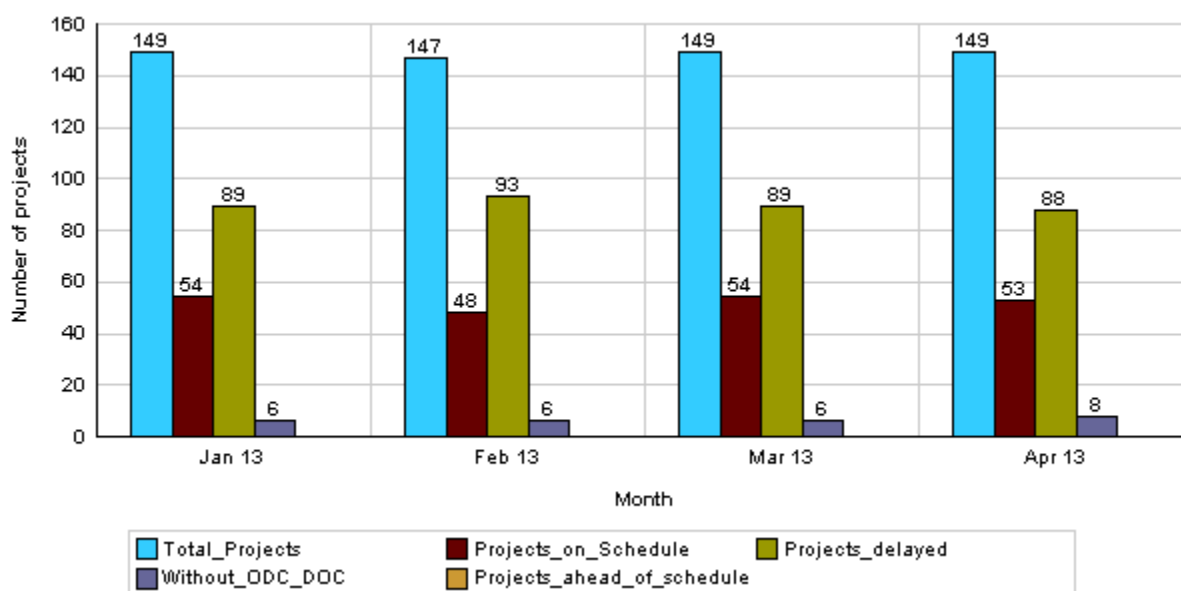


Break-up of 88 Delayed projects in April 2013

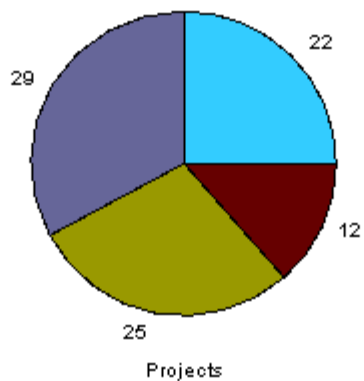


Delay in Months



Graphical Analysis of Railways Sector

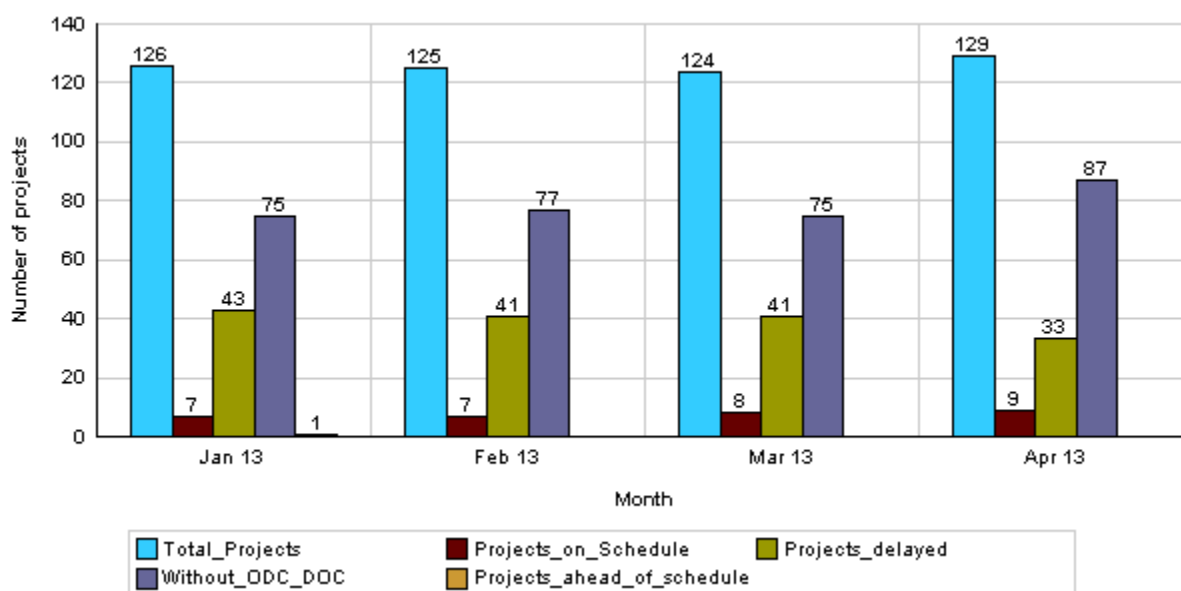


Break-up of 33 Delayed projects in April 2013

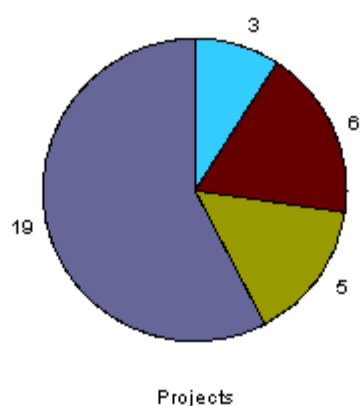


Delay in Months



Graphical Analysis of Power Sector

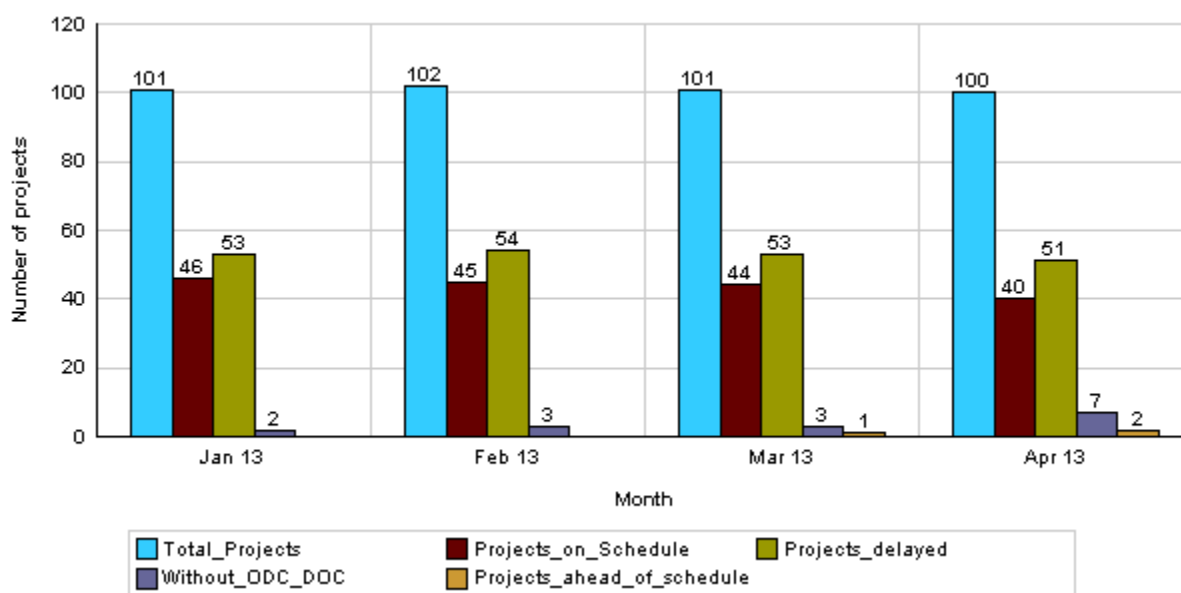


Break-up of 51 Delayed projects in April 2013

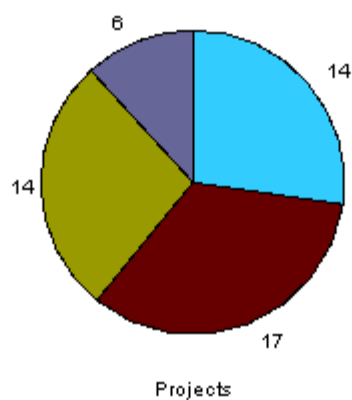


Delay in Months



Graphical Analysis of Petroleum Sector

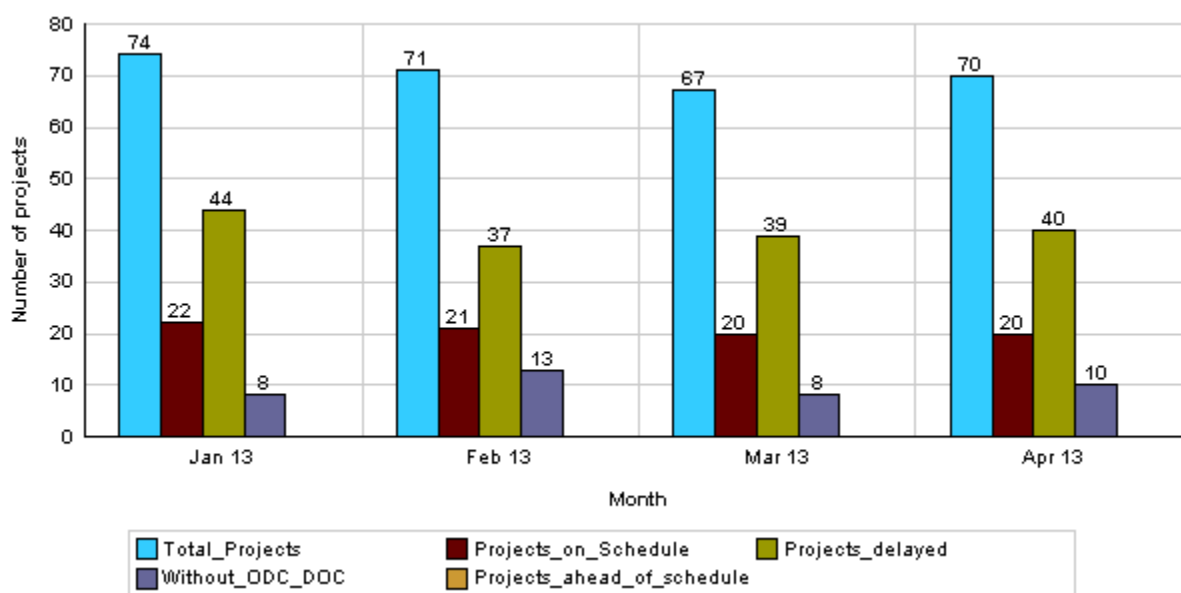


Break-up of 40 Delayed projects in April 2013

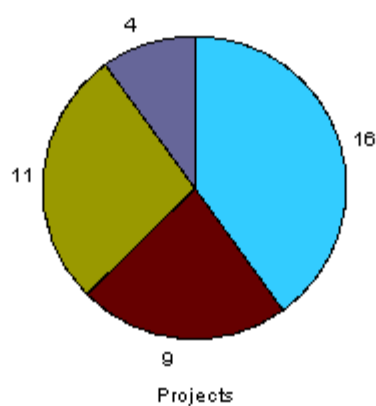


Delay in Months



Graphical Analysis of Steel Sector

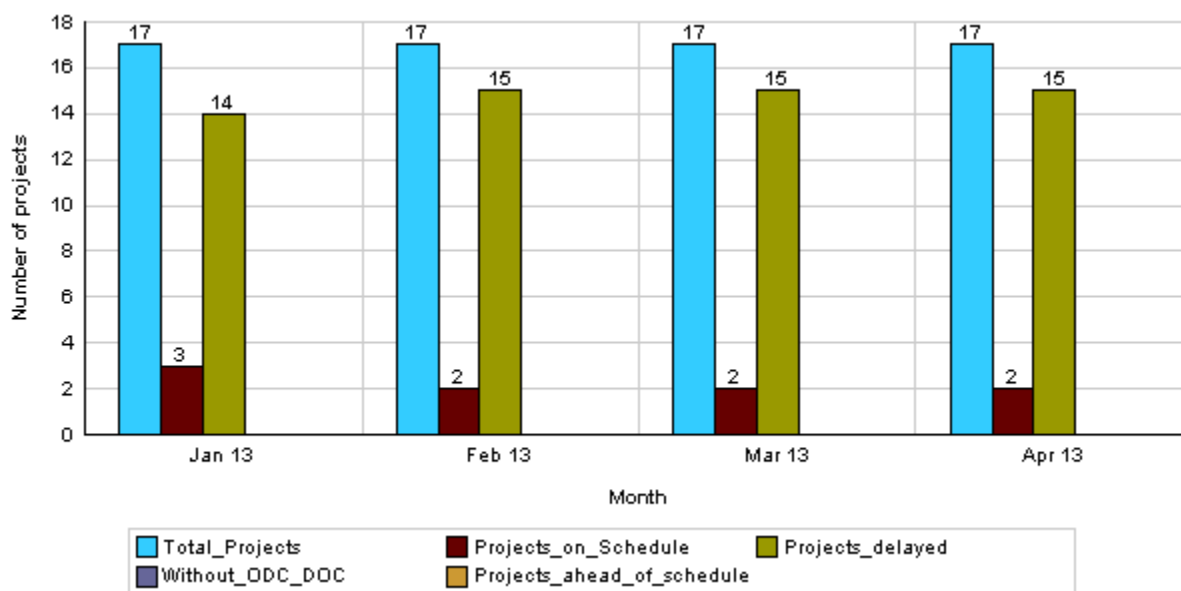


Break-up of 15 Delayed projects in April 2013

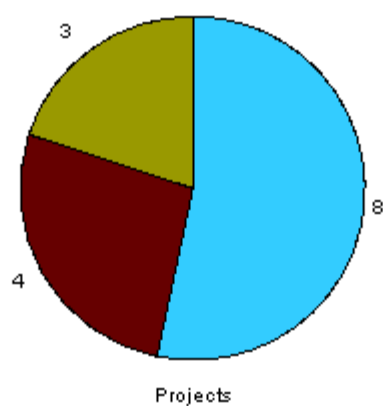


Delay in Months



Graphical Analysis of Coal Sector

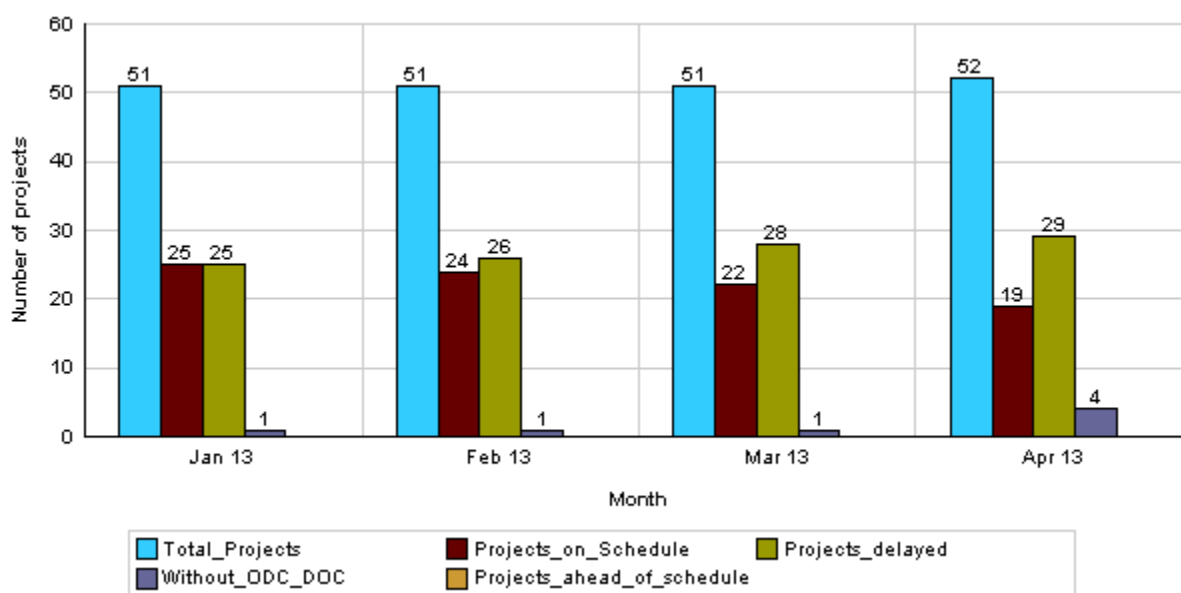


Break-up of 29 Delayed projects in April 2013

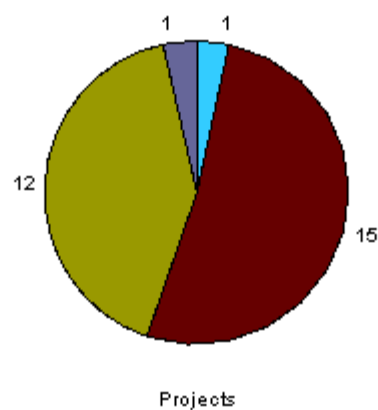


Delay in Months



Graphical Analysis of Civil Aviation Sector

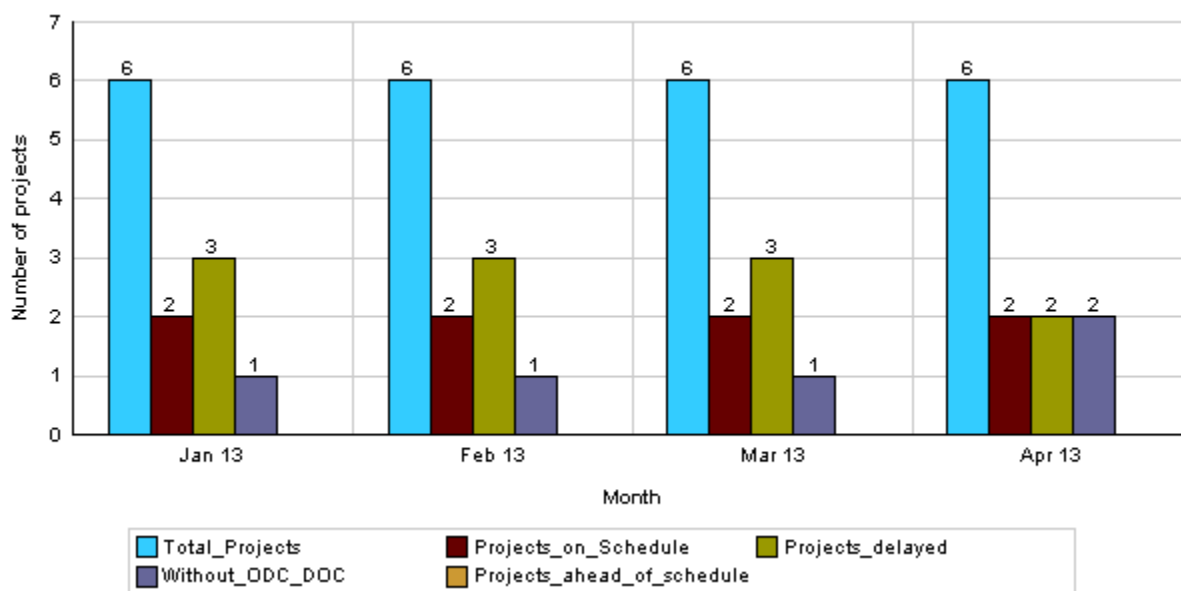


Break-up of 2 Delayed projects in April 2013

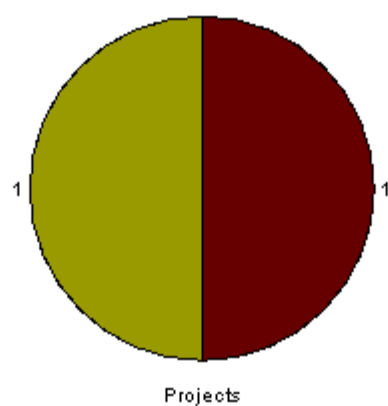

Delay in Months



Graphical Analysis of Atomic Energy Sector

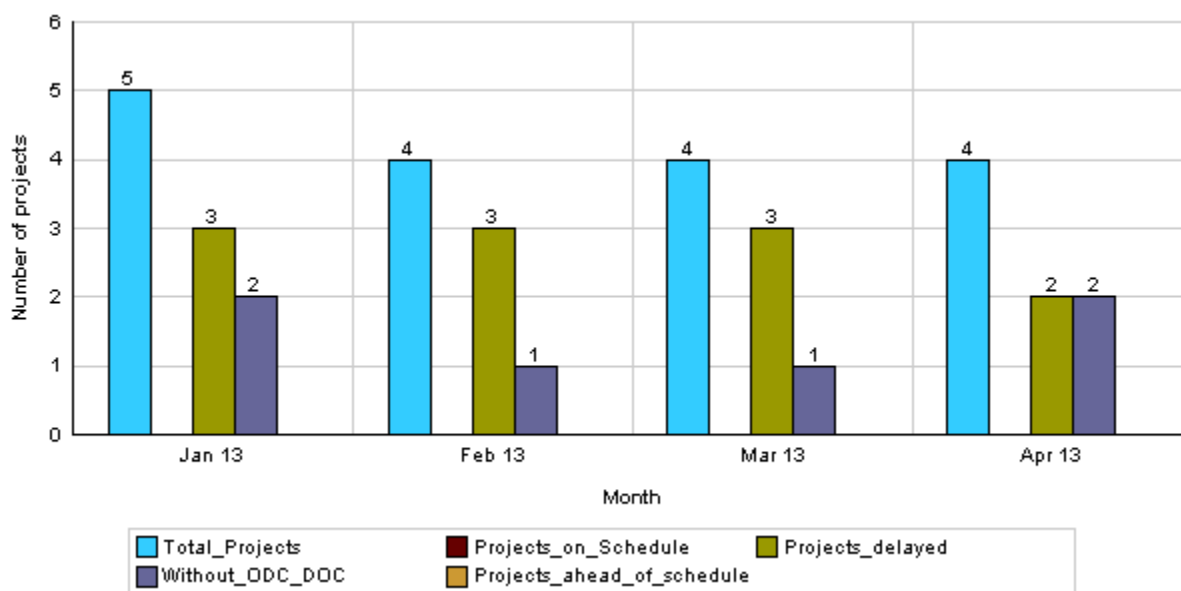

Break-up of 2 Delayed projects in April 2013



Delay in Months



Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. crore)			
		Original	Latest	Anticipated	Cumulative Expenditure
Atomic Energy	4	40,442.00	40,442.00	46,726.00	24,795.48
Civil Aviation	6	5,473.58	5,680.58	6,063.07	5,271.18
Coal	52	36,486.60	37,452.60	37,940.66	14,957.41
Fertilisers	1	1,478.63	1,478.63	1,478.63	1,087.00
Steel	17	65,285.87	67,562.15	71,443.41	48,647.59
Petrochemicals	1	5,460.61	8,920.00	8,920.00	4,510.51
Petroleum	70	165,950.52	179,674.08	178,609.86	83,622.41
Power	100	242,845.00	246,360.74	258,586.29	122,369.06
Railways	129	66,990.82	95,971.18	155,817.76	62,346.40
Road Transport & Highways	149	101,529.76	101,696.26	103,468.38	72,801.29
Shipping & Ports	19	15,617.12	17,389.43	17,902.42	8,260.18
Telecommunications	13	5,699.24	5,699.24	5,506.32	1,901.63
Urban Development	4	44,245.18	44,304.08	49,518.08	5,671.42
Water Resources	1	542.90	542.90	1,187.00	35.49
Grand total	566	798,047.83	853,173.87	943,167.88	456,277.05

Sector Wise Details

(Apr,2013)

S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs crore)	cumm expenditure	Date of Commissioning		Delay w.r.t. Original /Revised (in months)	Milestones Achieved / Total
						Original / Revised	Anticipated Cost		
1	2	3	4	5	6	7	8	9	10
Atomic Energy									
1	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00	11,459.00	2,771.00	12/2015	11/2016	11(O)	0/70
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00	17,270.00	16,007.00	12/2008	03/2013	-	39/106
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00	5,677.00	4,080.48	09/2010	-	-	8/82
4	RAJASTHAN ATOMIC POWER PROJECT -7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00	12,320.00	1,937.00	12/2016	03/2017	3(O)	0/69
Total			40,442.00	46,726.00	24,795.48				47/327
Civil Aviation									
5	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51	2,325.00	2,462.84	05/2011	03/2013	-	0/0
6	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46	309.46	226.70	01/2011 04/2013	12/2013	35(O) 8(R)	0/0
7	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61	335.61	208.92	05/2012	06/2013	13(O)	0/0
8	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	2,015.00	1,902.09	01/2011 02/2012	02/2012	-	0/0
9	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MO - [N04000070]AAI,Punjab	02/2011	452.00	452.00	93.66	03/2015	03/2015	0(O)	0/0
10	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00	626.00	376.97	06/2013	06/2013	0(O)	0/0
Total			5,473.58	6,063.07	5,271.18				0/0
Coal									
11	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	12/2009	212.34 779.26	977.53	704.17	03/2013 09/2012	07/2014	16(O) 22(R)	7/22
12	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N060000082]SECL,Chhatisgarh	11/2009	150.59	198.59	113.78	03/2016	03/2016	0(O)	2/6
13	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]NCL,Madhya pradesh	12/2009	1,352.04 1,143.54	1,143.54	437.14	03/2016 03/2016	03/2016	0(O) 0(R)	2/4

Sector Wise Details

(Apr,2013)

S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs crore)	cumulative expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved / Total
						Original / Revised	Anticipated Cost		
1	2	3	4	5	6	7	8	9	10
14	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Odisha	08/2008	207.28	207.28	102.56	03/2012	03/2014	24(O)	5/9
15	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhand	12/2007	471.66	341.63	236.63	03/2011	03/2014	36(O)	0/4
16	BALRAM OCP EXTENSION,MCL (8.00 Mty) - [N06000044]MCL,Odisha	12/2007	172.08	172.08	119.73	03/2010	03/2015	60(O)	4/5
17	BAROUD OC EXPANSION (RCE)-3MTY - [N06000099]SECL,Chhatisgarh	04/2012	258.56	258.56	42.62	03/2016	03/2016	0(O)	0/6
18	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]MCL,Odisha	12/2007	490.00	490.10	123.40	03/2017	03/2017	0(O)	6/12
19	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019]NCL,Multi State	11/2006	168.97	168.97	40.86	03/2014	03/2014	0(O)	1/4
20	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2011	746.04	535.10	170.09	03/2015	03/2015	0(O)	0/3
21	Batura OCP (2.0 MTY) - [N06000049]SECL,Madhya pradesh	09/2008	203.82	203.82	-	03/2015	03/2015	0(O)	1/2
22	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35	462.35	267.13	03/2014	03/2016	24(O)	2/8
23	Churi Benti UG (0.81 MTY) - [N06000083]CCL,Jharkhand	08/2007	163.51	163.51	34.96	03/2011	03/2016	60(O)	0/2
24	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,Chhatisgarh	12/2009	1,943.66	1,943.66	1,283.53	03/2014	03/2016	24(O)	6/12
25	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,Chhatisgarh	06/2010	2,675.67	2,675.67	1,445.34	03/2014	03/2016	24(O)	10/15
26	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,Odisha	02/2008	395.87	395.87	84.50	03/2015	03/2015	0(O)	2/12
27	HINGULA OC-II EXP PH-III (15 MTY) - [N06000068]MCL,Odisha	11/2008	479.63	479.63	126.19	03/2013	03/2015	24(O)	5/10
28	JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh	09/2008	152.43	152.43	-	03/2015	03/2017	24(O)	1/7
29	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,Andhra Pradesh	07/2011	447.06	447.06	3.02	03/2015	03/2015	0(O)	4/31
30	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	09/2007	467.78	467.78	12.31	03/2013	03/2013	-	4/83
31	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18	287.17	0.92	03/2011	03/2017	72(O)	0/2
32	KAKATIYA LONGWALL - [N06000048]SCCL,Andhra Pradesh	12/2008	453.63	453.63	84.10	12/2012	03/2016	39(O)	8/44
33	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Odisha	12/2007	457.77	457.77	113.13	03/2013	03/2015	24(O)	6/11
34	KARMA OCP (1.0MTY) - [N06000088]CCL,Jharkhand	06/2009	162.46	162.46	35.84	03/2014	03/2014	0(O)	0/3
35	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44	178.44	-	03/2014	03/2016	24(O)	1/7
36	KHADIA EXPANSION OPENCAST PROJECT 4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28	1,131.28	3.87	03/2018	03/2018	0(O)	0/3

Sector Wise Details

(Apr,2013)

S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs crore)	cumulative expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved / Total
						Original / Revised	Anticipated Cost		
1	2	3	4	5	6	7	8	9	10
37	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Uttar Pradesh	06/2011	789.88 741.62	741.62	366.34	03/2013 -	03/2014	12(O) -	2/5
38	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Odisha	01/2005	302.96 -	302.96	109.05	03/2010 -	03/2014	48(O) -	7/10
39	KUSMUNDA EXPN.OCP(SECL)(10-15)MTY - [N06000008]SECL,Chhatisgarh	06/2008	1,188.31 -	1,188.31	731.31	03/2013 -	03/2013	-	0/9
40	Kistaram OCP - [N06000089]SCCL,Andhra Pradesh	11/2010	242.29 -	242.29	-	03/2015 -	03/2015	0(O) -	0/28
41	MAGADH OC 20 MTY (CCL) - [N06000015]JCL,Jharkhand	08/2008	469.78 -	706.40	19.36	07/2012 -	03/2016	44(O) -	1/5
42	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,Chhatisgarh	12/2009	321.42 -	321.50	206.28	03/2014 -	03/2016	24(O) -	1/6
43	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19 -	181.19	34.29	03/2012 -	03/2015	36(O) -	7/20
44	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhand	08/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015	0(O) -	0/0
45	Muraidih UG - [N06000096]BCCL,Jharkhand	02/2011	339.88 -	339.88	-	04/2014 -	04/2014	0(O) -	0/0
46	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu	06/2011	5,907.11 -	5,907.11	28.94	12/2015 -	12/2017	24(O) -	0/33
47	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40 -	259.40	4.42	03/2012 -	03/2015	36(O) -	0/2
48	North Urimari OCP (3.0 MTY) - [N06000084]JCL,Jharkhand	12/2007	179.87 -	179.87	60.75	03/2012 -	03/2017	60(O) -	0/4
49	PELMA OCP(10.00MTY) - [N06000045]SECL,Chhatisgarh	07/2008	448.32 -	448.32	-	03/2015 -	03/2015	0(O) -	1/1
50	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77 -	339.77	0.91	03/2014 -	03/2016	24(O) -	0/1
51	Purnadih OCP (3.0 MTY) - [N06000085]JCL,Jharkhand	07/2008	210.98 -	210.98	91.63	03/2013 -	03/2015	24(O) -	2/4
52	RAJMAHAL OC EXP. - [N06000056]ECL,Jharkhand	09/2009	153.82 -	153.82	29.19	03/2014 -	03/2016	24(O) -	0/2
53	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97 -	418.97	200.01	03/2012 -	03/2015	36(O) -	24/27
54	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,Andhra Pradesh	07/2011	162.76 -	162.76	2.48	03/2015 -	03/2015	0(O) -	4/29
55	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,Andhra Pradesh	11/2012	430.14 -	430.14	56.84	- -	-	-	0/0
56	RKP OCP PHASE-I - [N06000079]SCCL,Andhra Pradesh	03/2010	209.78 -	209.78	30.77	03/2015 -	03/2015	0(O) -	4/31
57	Rajrappa RCE OCP (3.0 MTY) - [N06000087]JCL,Jharkhand	12/2009	510.85 -	510.85	269.09	03/2016 -	03/2016	0(O) -	1/4
58	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03 -	249.03	49.73	03/2012 -	-	-	11/42

Sector Wise Details

(Apr,2013)

S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs crore)	cum expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved / Total
						Original / Revised	Anticipated Cost		
1	2	3	4	5	6	7	8	9	10
59	TALABIRA OCP - [N06000043]MCL,Odisha	03/2008	447.72	447.72	44.50	03/2016	03/2016	0(O)	0/10
60	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 3,027.59	3,027.59	2,700.84	06/2009	01/2014	55(O)	20/24
61	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54	4,909.54	4,204.07	03/2012	03/2014	24(O)	19/39
62	Tapin OCP (2.5 MTY) - [N06000086]CCL,Jharkhand	08/2008	264.68	264.68	130.79	03/2012	03/2016	48(O)	0/4
	Total		36,486.60	37,940.66	14,957.41				181/667
	Fertilisers								
63	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,Punjab	01/2010	1,478.63	1,478.63	1,087.00	01/2013	03/2013	-	0/8
	Total		1,478.63	1,478.63	1,087.00				0/8
	Steel								
64	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,Karnataka	04/2011	572.00	572.00	273.70	04/2013 12/2013	12/2013	8(O) 0(R)	16/19
65	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00	350.00	241.50	08/2010	04/2013	32(O)	0/1
66	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00	343.58	246.84	02/2011	04/2013	26(O)	2/3
67	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,Karnataka	02/2011	898.55	898.55	197.17	05/2013 11/2013	11/2013	6(O) 0(R)	12/21
68	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00	450.00	190.54	05/2012	06/2013	13(O)	1/2
69	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89 607.17	607.17	349.79	12/2011 03/2012	12/2013	24(O) 21(R)	16/21
70	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	08/2007	108.00	216.68	77.01	10/2012	06/2013	8(O)	3/4
71	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, chatisgarh - [N12000078]SAIL,Chhatisgarh	07/2012	332.65	332.65	49.35	08/2014	08/2014	0(O)	0/0
72	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON - [N12000075]SAIL,Odisha	11/2011	254.55	254.55	50.86	11/2013	03/2014	4(O)	1/1
73	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	17,265.00	17,265.00	8,710.58	03/2013	03/2014	12(O)	22/27
74	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhand	01/2008	6,325.00	6,325.00	3,491.74	12/2011	12/2013	24(O)	16/16

Sector Wise Details

(Apr,2013)

S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs crore)	cumulative expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved / Total
						Original / Revised	Anticipated Cost		
1	2	3	4	5	6	7	8	9	10
75	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL, West Bengal	06/2009	2,875.00	2,875.00	1,542.96	12/2012	12/2013	12(O)	10/12
76	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL, West Bengal	02/2008	14,443.00	16,408.00	14,571.32	12/2011	12/2013	24(O)	19/19
77	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL, Andhra Pradesh	10/2005	8,692.00	12,291.00	9,481.85	10/2009	06/2013	44(O)	62/64
78	Expansion of Rourkela Steel Plant - [N12000056]SAIL, Odisha	09/2008	11,812.00	11,812.00	9,098.52	03/2013	12/2013	9(O)	11/14
79	INSTALLATION OF 1x45 MVA Submerged Arc Furnace AT - [N12000076]SAIL, Maharashtra	12/2011	187.33	187.33	70.98	10/2013	03/2014	5(O)	0/1
80	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Oddisha - [N12000079]SAIL, Odisha	01/2012	254.90	254.90	2.88	12/2014	12/2014	0(O)	0/0
Total			65,285.87	71,443.41	48,647.59				191/225
<u>Petrochemicals</u>									
81	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, Assam	04/2006	5,460.61	8,920.00	4,510.51	04/2012	12/2013	20(O)	19/29
Total			5,460.61	8,920.00	4,510.51				19/29
<u>Petroleum</u>									
82	102 MW WIND POWER PROJECT - [N16000119]ONGC, Rajasthan	07/2010	1,106.00	678.02	-	06/2012	03/2014	21(O)	0/0
83	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC, Multi State	01/2010	2,163.64	2,163.64	1,557.08	06/2012	06/2013	12(O)	0/0
84	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC, Maharashtra	10/2008	1,797.35	977.00	726.73	12/2011	07/2013	19(O)	0/0
85	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, Assam	03/2009	2,465.15	2,378.86	1,410.63	03/2013	03/2014	12(O)	0/0
86	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL, Multi State	08/2011	586.00	586.00	5.53	07/2015	08/2015	1(O)	0/0
87	Ahmedabad Redevelopment - [N16000120]ONGC, Gujarat	11/2010	1,916.10	1,916.10	783.72	12/2014	12/2014	0(O)	0/0
88	Ankleswar Redevelopment - [N16000122]ONGC, Gujarat	11/2010	2,189.63	2,189.63	1,039.14	12/2014	12/2014	0(O)	0/0
89	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL, Multi State	12/2009	540.92	540.92	206.52	07/2012	-	-	0/17
90	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]IOCL, Haryana	11/2009	341.50	341.50	172.12	02/2013	06/2013	4(O)	38/42
91	Butene-1 at Panipat - [N16000139]IOCL, Haryana	02/2012	190.00	190.00	43.53	03/2014	03/2014	0(O)	0/24

Sector Wise Details

(Apr,2013)

S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs crore)	cum expenditure	Date of Commissioning		Delay w.r.t. Original /Revised (in months)	Milestones Achieved / Total
						Original / Revised	Anticipated Cost		
1	2	3	4	5	6	7	8	9	10
92	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65	736.65	344.95	09/2011	12/2013	27(O)	0/0
93	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00	394.00	312.61	-	03/2013	-	18/19
94	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79	761.68	273.53	05/2013	11/2013	6(O)	0/0
95	Capacity Augmentation of Kota Piyala Section of MMBPL Pipeli - [N16000153]BPCL,Rajasthan	04/2011	152.89	152.89	105.27	06/2013	06/2013	0(O)	0/0
96	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20	269.10	35.90	08/2013	01/2014	5(O)	0/0
97	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26	240.95	95.34	09/2012	09/2013	12(O)	0/0
98	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64	723.64	-	03/2013	11/2013	8(O)	0/0
99	DBPL-II - [N16000147]GAIL,Multi State	06/2009	486.00	486.00	46.16	09/2013	09/2013	0(O)	0/0
100	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00	1,584.00	315.84	-	-	-	0/0
101	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82	2,735.65	2,184.00	04/2006	06/2013	86(O)	0/0
102	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78	5,633.44	4,464.10	08/2010	12/2013	40(O)	0/0
103	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40	2,920.82	1,881.73	09/2010	06/2013	33(O)	0/0
104	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21	1,436.21	920.79	07/2010	05/2013	34(O)	0/0
105	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16	3,690.37	2,520.91	12/2008	06/2013	54(O)	0/0
106	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00	2,174.00	1,425.10	09/2011	06/2013	21(O)	5/76
107	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00	2,730.00	1,663.16	09/2011	06/2013	21(O)	54/59
108	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11	372.11	215.02	03/2013	06/2013	3(O)	0/0
109	Development of C-26 Cluster Fields - [N16000133]ONGC,Maharashtra	03/2012	2,592.17	2,592.17	-	05/2014	05/2014	0(O)	0/0
110	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03	5,916.65	1,301.61	03/2013	04/2014	13(O)	0/0

Sector Wise Details

(Apr,2013)

S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs crore)	cumulative expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved / Total
						Original / Revised	Anticipated Cost		
1	2	3	4	5	6	7	8	9	10
111	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44	410.44	210.57	11/2012	10/2013	11(O)	0/0
112	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00	2,523.00	883.68	01/2014	01/2014	0(O)	0/0
113	Development of Western Periphery of MH South Field - [N16000136]ONGC,Multi State	04/2012	600.17	600.17	51.17	12/2014	12/2014	0(O)	0/0
114	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00	1,000.00	477.65	01/2013	09/2013	8(O)	18/18
115	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MU - [N16000081]BPCL,Maharashtra	04/2008	825.00	1,827.00	1,433.73	04/2013	06/2013	2(O)	0/167
116	Heera and South Heera Redevelopment Ph-II - [N16000132]ONGC,Maharashtra	03/2012	5,608.40	5,608.40	712.11	05/2015	05/2015	0(O)	0/0
117	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09	1,674.11	1,556.44	03/2007	03/2017	120(O)	6/6
118	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10	663.69	637.21	03/2007	03/2014	84(O)	3/3
119	IOR of B-173A Field - [N16000140]ONGC,Multi State	01/2012	352.49	352.49	-	03/2014	04/2014	1(O)	0/0
120	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90	438.85	296.85	03/2006	06/2013	87(O)	6/6
121	IROP - [N16000143]BPCL,Kerala	01/1999	14,225.00	14,225.00	341.26	12/2015	05/2016	5(O)	0/0
122	Integrated Development of B-127 fields - [N16000131]ONGC,Maharashtra	12/2011	2,059.63	2,665.65	113.16	03/2015	03/2015	0(O)	0/0
123	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18	6,652.22	2.20	01/2013	-	-	0/0
124	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07	281.07	3.41	10/2010	12/2014	50(O)	0/0
125	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- - [N16000070]GAIL,Multi State	07/2009	238.68	204.00	172.59	01/2012	-	-	0/1
126	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJEC - [N16000129]GAIL,Multi State	06/2009	2,915.00	2,300.00	790.60	12/2012	-	-	0/21
127	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,Karnataka	11/2012	666.00	666.00	-	11/2015	11/2015	0(O)	0/0
128	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00	12,160.26	10,160.83	01/2012	05/2013	16(O)	0/108
129	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39	6,855.93	5,124.72	09/2012	09/2013	12(O)	0/0
130	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03	8,813.41	7,204.61	05/2010	06/2013	37(O)	0/0
131	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00	3,823.00	701.81	04/2015	04/2015	0(O)	0/0

Sector Wise Details

(Apr,2013)

S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs crore)	cumulative expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved / Total
						Original / Revised	Anticipated Cost		
1	2	3	4	5	6	7	8	9	10
132	Mounded Bullet - [N16000154]CPCL,Tamil Nadu	12/2012	279.00	279.00	-	12/2014	12/2014	0(O)	0/0
133	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70	973.79	729.51	03/2011	05/2013	26(O) 24(R)	0/0
134	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02	740.02	704.59	03/2010 03/2012	05/2013	38(O) 14(R)	0/0
135	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,Multi State	02/2011	913.00	913.00	23.69	07/2015	07/2015	0(O)	0/0
136	PARADIP REFINERY PROJECT - [N16000058]IOCL,Odisha	02/2009	29,777.00	32,710.00	21,447.00	11/2012	03/2014	16(O)	60/100
137	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,Multi State	08/2009	1,793.00	1,793.00	790.46	09/2012	-	-	5/11
138	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00	8,140.00	1,944.63	02/2014	02/2014	0(O)	0/0
139	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	08/2009	246.81 276.83	276.83	223.40	04/2012	06/2013	14(O)	0/0
140	Pipeline Replacement Project-3 - [N16000137]ONGC,Multi State	04/2012	2,547.26	1,417.00	336.94	05/2014	05/2014	0(O)	0/0
141	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78	1,803.78	571.09	07/2012	10/2013	15(O)	0/31
142	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 898.00	898.00	986.69	-	08/2013	-	52/53
143	REWARI KANPUR PIPELINE PROJECT - [N16000145]HPCL,Multi State	02/2012	1,210.64	1,210.64	60.89	11/2015	11/2015	0(O)	4/25
144	Replacement of CDU/VDU at Mumbai Refinery - [N16000142]BPCL,Maharashtra	01/1999	1,419.00	1,419.00	56.84	12/2014	12/2014	0(O)	0/0
145	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]Mangalore Refin,Karnataka	07/2010	1,043.57	1,043.57	378.80	04/2012	-	-	0/0
146	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]SPRL,Karnataka	01/2006	732.00 1,227.00	1,227.00	-	10/2011	12/2013	26(O)	0/0
147	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]SPRL,Andhra Pradesh	01/2006	672.00 1,038.00	1,038.00	-	10/2011	12/2013	26(O)	0/0
148	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,Multi State	11/2012	309.81	309.81	-	08/2014	08/2014	0(O)	0/0
149	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	253.66	170.77	08/2012	06/2013	10(O)	0/0
150	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32	330.47	207.24	03/2012	-	-	13/20

Sector Wise Details

(Apr,2013)

S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs crore)	cumulative expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved / Total
						Original	Anticipated		
1	2	3	4	5	6	7	8	9	10
151	Wax Project - [N16000101]NRL,Assam	06/2010	576.60	576.60	64.25	12/2013	12/2013	0(O)	0/0
			-	-	-	-	-	-	-
	Total		165,950.52	178,609.86	83,622.41				282/807
			-	-	-				
	Power								
152	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33	7,075.33	5,769.30	08/2012	03/2014	19(O)	0/11
			-	-	-	-	-	-	-
153	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32	1,347.32	1,205.60	02/2012	05/2013	15(O)	0/4
			-	-	-	-	-	-	-
154	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12	1,075.12	813.80	05/2012	09/2013	16(O)	0/8
			-	-	-	-	-	-	-
155	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36	1,736.36	1,408.00	06/2012	05/2013	11(O)	0/4
			-	-	-	-	-	-	-
156	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]PGCIL,Multi State	12/2012	156.04	156.04	-	10/2014	10/2014	0(O)	0/7
			-	-	-	-	-	-	-
157	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04	7,341.04	5,948.00	08/2013	09/2014	13(O)	8/19
			-	-	-	-	-	-	-
158	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97	8,693.00	8,407.00	12/2009	02/2017	86(O)	27/47
			-	-	-	-	-	-	-
159	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35	4,375.35	3,797.00	07/2011	10/2015	51(O)	5/28
			-	-	-	-	-	-	-
160	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,Jammu and Kashmir	08/2006	621.26	913.00	731.93	02/2011 10/2012	01/2013	-	2/4
			-	-	-	-	-	-	-
161	COMMON SYS. ASSOCIATED PART- B - [N18000144]PGCIL,Multi State	03/2013	2,514.88	2,514.88	-	12/2015	12/2015	0(O)	0/20
			-	-	-	-	-	-	-
162	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNA - [N18000111]PGCIL,Andhra Pradesh	08/2011	1,637.34	1,637.34	652.10	08/2014	08/2014	0(O)	7/20
			-	-	-	-	-	-	-
163	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA - [N18000126]PGCIL,Andhra Pradesh	03/2012	206.44	206.44	39.10	06/2014	06/2014	0(O)	0/20
			-	-	-	-	-	-	-
164	COMMON TR. SYS. ASSOCIATED WITH EAST A.P - [N18000143]PGCIL,Multi State	03/2013	514.20	514.20	-	06/2015	06/2015	0(O)	0/0
			-	-	-	-	-	-	-
165	COMMON TRANSMISSION SCHEME WITH ISSG - [N18000139]PGCIL,Tamil Nadu	01/2013	182.80	182.80	3.60	10/2014	10/2014	0(O)	0/0
			-	-	-	-	-	-	-
166	Common System Associated with Coastal Energen Priv - [N18000103]PGCIL,Tamil Nadu	09/2011	1,940.13	1,940.13	803.30	09/2014	09/2014	0(O)	7/20
			-	-	-	-	-	-	-

Sector Wise Details

(Apr,2013)

S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs crore)	cumulative expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved / Total
						Original	Anticipated		
1	2	3	4	5	6	7	8	9	10
167	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96	975.96	881.10	10/2009	09/2013	47(O)	5/15
168	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80	1,272.80	619.70	11/2012	09/2014	22(O)	2/13
169	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123]PGCIL,Multi State	03/2012	198.63	198.63	-	09/2014	09/2014	0(O)	0/0
170	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA - [N18000101]PGCIL,Chhatisgarh	05/2011	1,961.87	1,961.87	888.90	05/2014	05/2014	0(O)	1/11
171	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52	1,719.52	1,068.30	08/2013	08/2013	0(O)	1/12
172	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,Bihar	12/2011	901.77	901.77	186.90	08/2014	08/2014	0(O)	1/16
173	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000107]PGCIL,Chhatisgarh	08/2011	1,391.97	1,391.97	906.80	12/2013	12/2013	0(O)	1/12
174	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32	160.32	72.00	10/2012	05/2013	7(O)	4/14
175	KAIGA 3 and 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45 1,007.16	1,007.16	898.93	12/2007 12/2009	-	-	2/11
176	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pradesh	12/2004	2,496.90	2,496.90	2,242.30	05/2013 06/2016	03/2017	46(O) 9(R)	7/22
177	KISHANGANGA HEP - [N18000031]NHPC,Jammu and Kashmir	07/2007	2,238.67 3,642.04	3,642.00	1,412.13	01/2016 01/2016	11/2016	10(O) 10(R)	0/4
178	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pradesh	10/2002	4,527.15	6,358.91	4,940.00	04/2009	09/2014	65(O)	0/9
179	KUDGI STPP STAGE 1 - [N18000131]NTPC,Karnataka	12/2011	15,166.19	15,166.19	1,525.00	12/2016	12/2016	0(O)	7/11
180	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29 2,159.07	2,159.07	1,868.51	09/2008	03/2013	-	15/23
181	LARA STPP STAGE-I - [N18000140]NTPC,Chhatisgarh	11/2012	11,846.00	11,846.00	1,053.00	05/2017	05/2017	0(O)	4/4
182	Lata-Tapovan HPP 3x57MW - [N18000142]NTPC,Uttarakhand	07/2012	1,527.00	1,527.00	83.89	08/2017	08/2017	0(O)	0/15
183	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28	6,010.89	5,315.00	08/2012	03/2013	-	16/16
184	MOUDA STPP STAGE 2 - [N18000132]NTPC,Maharashtra	03/2012	7,921.47	7,921.47	913.00	09/2016	09/2016	0(O)	13/14
185	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,Jammu and Kashmir	08/2006	611.01	936.00	730.06	08/2010 01/2013	10/2013	38(O) 9(R)	0/3

Sector Wise Details

(Apr,2013)

S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs crore)	cumulative expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved / Total
						Original	Anticipated		
1	2	3	4	5	6	7	8	9	10
186	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19	11,130.19	5,845.80	08/2013	06/2015	22(O)	0/17
187	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29	410.29	266.30	02/2012	12/2013	22(O)	1/13
188	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48	520.48	352.20	11/2011	07/2014	32(O)	0/11
189	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66	509.66	362.90	11/2011	12/2013	25(O)	1/14
190	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68	182.68	130.20	01/2013	09/2013	8(O)	1/6
191	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64	752.64	258.40	07/2013	03/2014	8(O)	1/11
192	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57	1,677.57	800.40	04/2013	03/2014	11(O)	0/11
193	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,Multi State	11/2011	723.63	723.63	129.40	11/2014	11/2014	0(O)	1/12
194	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]PGCIL,Multi State	09/2012	803.34	803.34	69.00	03/2015	03/2015	0(O)	0/15
195	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,Multi State	09/2012	524.40	524.40	23.20	04/2015	05/2015	1(O)	0/16
196	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58	965.58	550.20	11/2012	03/2014	16(O)	0/11
197	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pradesh	10/2005	2,304.56	2,716.00	1,788.15	10/2010	03/2014	41(O)	0/6
198	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pradesh	09/2002	3,919.59	5,366.00	3,420.65	09/2009	03/2018	102(O)	1/20
199	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pradesh	12/2008	573.99	573.99	542.85	08/2012	09/2014	25(O)	16/22
200	RAMPUR HEP(412 MW) - [N18000024]SJVN,L,Himachal Pradesh	01/2007	2,047.03	2,047.03	2,375.16	01/2012	03/2014	26(O)	0/27
201	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81	6,230.81	4,283.00	10/2012	11/2013	13(O)	12/16
202	SOLAPUR STTP - [N18000133]NTPC,Maharashtra	03/2012	9,395.18	9,395.18	1,450.00	11/2016	11/2016	0(O)	13/14
203	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pradesh	09/2003	6,285.33	10,667.00	5,653.55	09/2010	12/2017	87(O)	11/11

Sector Wise Details

(Apr,2013)

S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs crore)	cumulative expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved / Total
						Original	Anticipated		
1	2	3	4	5	6	7	8	9	10
204	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36	170.36	81.30	04/2013	09/2013	5(O)	4/15
205	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95	2,360.95	2,047.40	08/2012	03/2014	19(O)	0/5
206	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,Multi State	09/2012	1,508.74	1,508.74	49.70	06/2016	04/2015	-14(O)	0/20
207	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,Multi State	09/2012	1,935.35	1,935.35	157.10	12/2014	11/2014	-1(O)	0/0
208	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BA - [N18000124]PGCIL,Madhya Pradesh	03/2012	213.78	213.78	-	03/2014	03/2014	0(O)	0/7
209	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR - [N18000116]PGCIL,Chhatisgarh	12/2011	1,746.65	1,746.65	86.30	08/2014	08/2014	0(O)	2/19
210	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP P - [N18000120]PGCIL,Maharashtra	02/2012	1,310.85	1,310.85	283.00	02/2015	02/2015	0(O)	0/14
211	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,Multi State	06/2012	1,263.26	1,263.26	134.20	11/2014	11/2014	0(O)	0/16
212	SYSTEM STRENGTHENING IN RAIPUR- WARDHA CORRIDOR FOR IPP PROJEC - [N18000117]PGCIL,Chhatisgarh	01/2012	1,422.85	1,422.85	252.70	01/2015	01/2015	0(O)	3/19
213	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,Multi State	12/2011	297.33	297.33	91.50	08/2014	08/2014	0(O)	7/20
214	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,Multi State	10/2011	487.49	487.49	135.10	06/2014	06/2014	0(O)	7/20
215	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34	232.34	147.58	06/2012	06/2013	12(O)	0/3
216	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83	1,216.83	859.00	08/2012	06/2014	22(O)	0/11
217	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttarakhand	11/2006	2,978.48	2,978.48	1,809.00	03/2013	03/2016	36(O)	2/15
218	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38	1,501.75	1,116.04	09/2009 06/2013	05/2014	56(O) 11(R)	0/0
219	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92	1,628.00	1,486.94	03/2007 09/2012	04/2013	73(O) 7(R)	25/25
220	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00 2,978.88	2,978.86	477.93	07/2010 02/2016	11/2016	76(O) 9(R)	1/10

Sector Wise Details

(Apr,2013)

S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs crore)	cumm expenditure	Date of Commissioning		Delay w.r.t. Original /Revised (in months)	Milestones Achieved / Total
						Original / Revised	Anticipated Cost		
1	2	3	4	5	6	7	8	9	10
221	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000118]PGCIL,Gujarat	01/2012	259.28	259.28	82.50	01/2014	01/2014	0(O)	3/18
222	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKH - [N18000113]PGCIL,Multi State	12/2011	2,422.66	2,422.66	264.90	08/2014	08/2014	0(O)	2/19
223	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART - - [N18000129]PGCIL,Multi State	02/2012	3,201.44	3,201.44	541.70	10/2014	10/2014	0(O)	2/18
224	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12	4,824.12	3,354.60	10/2012	03/2014	17(O)	0/11
225	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR - [N18000077]PGCIL,West Bengal	04/2010	4,404.57	4,404.57	370.90	01/2015	01/2015	0(O)	0/20
226	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL,Multi State	03/2011	2,569.25	2,569.25	1,445.90	03/2014	03/2014	0(O)	4/15
227	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000121]PGCIL,Andhra Pradesh	02/2012	324.33	324.33	19.50	08/2014	08/2014	0(O)	7/20
228	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000122]PGCIL,Andhra Pradesh	02/2012	1,927.16	1,927.16	238.70	10/2014	10/2014	0(O)	3/16
229	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pradesh	07/2006	557.24	758.75	638.60	01/2010	06/2013	41(O)	2/11
230	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19	184.19	156.80	11/2011	09/2013	22(O)	0/4
231	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88	7,031.88	4,430.20	12/2012	12/2013	12(O)	0/9
232	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT - [N18000114]PGCIL,Gujarat	12/2011	552.44	552.44	234.20	02/2014	02/2014	0(O)	3/17
233	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,Madhya pradesh	08/2011	425.51	425.51	282.60	10/2013	10/2013	0(O)	2/13
234	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93	181.93	48.90	07/2013	07/2013	0(O)	0/13
235	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CH - [N18000105]PGCIL,Multi State	09/2011	1,366.34	1,366.34	547.60	12/2013	12/2013	0(O)	2/13
236	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECT - [N18000104]PGCIL,Jharkhand	10/2011	558.26	558.26	139.90	11/2013	09/2014	10(O)	7/20

Sector Wise Details

(Apr,2013)

S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs crore)	cum expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved / Total
						Original / Revised	Anticipated Cost		
1	2	3	4	5	6	7	8	9	10
237	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Odisha	09/2010	2,074.86	2,074.86	1,000.50	03/2013	03/2014	12(O)	4/15
238	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Odisha	12/2010	2,743.19	2,743.19	1,447.80	12/2013	03/2014	3(O)	0/13
239	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99	4,672.99	2,532.40	11/2012	03/2015	28(O)	0/15
240	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR - [N18000112]PGCIL,Chhatisgarh	11/2011	2,127.51	2,127.51	735.80	07/2014	07/2014	0(O)	2/14
241	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01	623.44	527.59	-	07/2013	-	10/29
242	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,Mizoram	01/2011	913.63	913.63	412.59	07/2014	02/2015	7(O)	1/16
243	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00	2,144.00	1,258.80	12/2012	03/2014	15(O)	0/11
244	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL,Multi State	03/2011	1,585.12	1,585.12	837.80	11/2013	12/2014	13(O)	5/16
245	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03	250.03	62.70	01/2013	12/2014	23(O)	5/18
246	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,Jammu and Kashmir	08/2005	1,729.29	2,081.00	1,719.99	11/2009 02/2013	05/2013	42(O) 3(R)	0/4
247	VINDHYACHAL STPP STAGE-V - [N18000134]NTPC,Madhya pradesh	12/2011	3,180.40	3,180.40	274.00	08/2015	08/2015	0(O)	6/12
248	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00	5,915.00	4,637.00	10/2012	03/2013	-	15/15
249	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttarakhand	08/2008	2,491.58	3,422.44	346.69	07/2014	05/2016	22(O)	1/1
250	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69	477.69	437.30	09/2010	03/2013	-	0/5
251	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,Chhatisgarh	03/2012	9,569.76	9,569.76	640.20	06/2015	06/2015	0(O)	3/28
Total			242,845.00	258,586.29	122,369.06				333/1358
<u>Railways</u>									
252	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34	1,141.75	469.62	03/2014	12/2015	21(O)	0/0

Sector Wise Details

(Apr,2013)

S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs crore)	cumulative expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved / Total
						Original / Revised	Anticipated Cost		
1	2	3	4	5	6	7	8	9	10
253	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 427.21	432.72	372.21	12/2009 03/2011	10/2013	46(O) 31(R)	0/0
254	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 514.68	2,820.00	150.23	- -	-	-	0/0
255	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	435.87	396.76	03/2011 03/2011	03/2011	-	0/0
256	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 663.10	725.00	547.73	06/1999 03/2011	03/2011	-	0/0
257	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,Uttar Pradesh	03/2013	307.00 -	307.00	-	- -	-	-	0/0
258	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	1,214.00	96.96	- -	-	-	0/0
259	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,Uttar Pradesh	03/2012	160.89 -	199.75	36.94	- -	-	-	0/0
260	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.14 385.60	404.39	3.77	03/2013 -	03/2013	-	0/0
261	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 901.62	901.62	0.35	- -	-	-	0/0
262	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,028.05	1,423.98	472.32	03/2005 12/2008	12/2016	141(O) 96(R)	0/0
263	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15 1,106.62	1,106.62	224.41	12/2010 03/2011	03/2011	-	0/0
264	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	1,512.86	216.63	03/2004 12/2010	03/2016	144(O) 63(R)	0/0
265	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	2,384.34	49.34	04/2014 -	03/2017	35(O) -	0/0
266	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,Uttar Pradesh	03/2008	195.64 -	195.64	63.83	- -	-	-	0/0
267	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	800.00	718.89	03/2010 -	12/2015	69(O) -	0/0
268	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	4,996.65	2,724.46	04/2008 03/2014	12/2015	92(O) 21(R)	0/0
269	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 207.52	207.52	158.71	12/2012 -	12/2013	12(O) -	0/0
270	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	196.95	188.47	03/2011 -	-	-	0/0
271	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24 -	468.62	0.99	03/2012 -	-	-	0/0
272	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	579.37	599.40	- -	02/2012	-	0/0
273	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241]NR,Punjab	07/1998	248.44 576.27	1,115.21	951.56	12/2012 01/2013	02/2013	-	0/0

Sector Wise Details

(Apr,2013)

S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs crore)	cumulative expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved / Total
						Original / Revised	Anticipated Cost		
1	2	3	4	5	6	7	8	9	10
274	CHHAPRA-BALLIA UP - [N22000134]NER,Multi State	03/2013	295.00	295.00	0.06	-	-	-	0/0
275	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	1,417.97	1,011.09	-	03/2012	-	0/0
276	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79	585.93	194.91	-	12/2013	-	0/0
277	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,Multi State	03/2007	243.78	243.78	25.59	-	-	-	0/0
278	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pradesh	09/1996	156.00 156.00	406.40	328.82	-	06/2013	-	0/0
279	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00	968.60	126.84	12/2012	-	-	0/0
280	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar	04/2001	104.79	406.92	95.45	-	-	-	0/0
281	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	178.14	-	03/2013	-	0/0
282	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	607.09	484.04	12/2012 12/2012	02/2013	-	0/0
283	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]JR,Tamil Nadu	09/2006	343.17 343.17	914.98	625.68	-	12/2012	-	0/0
284	Dakshin-barasal-lakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	533.38	95.48	12/2011 02/2012	02/2012	-	0/0
285	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,West Bengal	03/2013	4,874.58	4,874.58	-	03/2016	03/2016	0(O)	0/0
286	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 224.89	246.44	141.55	03/2012 12/2013	03/2014	24(O) 3(R)	0/0
287	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,Uttar Pradesh	09/2001	129.70 245.39	245.39	210.67	12/2008	09/2014	69(O)	0/0
288	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74	495.74	244.64	06/2013 06/2013	12/2014	18(O) 18(R)	0/0
289	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	634.13	550.42	03/1995	03/2013	-	0/0
290	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	270.00	278.46	02/2011 02/2011	03/2013	-	0/0
291	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92	280.00	116.77	02/2006	-	-	0/0
292	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 381.17	863.23	626.57	-	03/2012	-	0/0
293	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	1,038.00	590.26	03/1998	-	-	0/0

Sector Wise Details

(Apr,2013)

S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs crore)	cumulative expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved / Total
						Original / Revised	Anticipated Cost		
1	2	3	4	5	6	7	8	9	10
294	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	776.00	338.76	- 05/2009	05/2009	-	0/0
295	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,Multi State	04/1986	158.77 580.83	580.83	558.78	03/1994 -	10/2013	235(O) -	0/0
296	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	611.03	124.23	12/2011 11/2013	11/2013	23(O) 0(R)	0/0
297	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	528.65	186.09	- -	-	-	0/0
298	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Odisha	04/1996	301.64 -	1,185.64	195.65	- 09/2009	-	-	0/0
299	HARNOUT -SET,UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	337.30	222.07	- -	03/2012	-	0/0
300	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	412.91	609.63	- -	01/2013	-	0/0
301	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	230.03	145.76	- -	03/2014	- -	0/0
302	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	535.40	175.57	03/2007 03/2007	03/2015	96(O) 96(R)	0/0
303	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1997	227.00 997.58	2,135.00	71.68	- -	-	-	0/0
304	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 829.74	829.74	3.08	03/2015 -	03/2015	0(O) -	0/0
305	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,Multi State	03/2002	409.00 625.30	847.75	841.01	06/2007 -	06/2007	-	0/0
306	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	1,043.56	694.03	03/2012 08/2012	-	-	0/0
307	JIND-SONEPAT (NL),NR - [220100280]NR,Haryana	01/2004	190.81 238.56	693.39	441.77	03/2012 03/2012	12/2012	-	0/0
308	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	4,453.50	1,370.28	03/2011 03/2014	03/2017	72(O) 36(R)	0/0
309	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 653.19	653.46	94.86	03/2014 -	03/2014	0(O) -	0/0
310	KADUR-CHIKMAGALUR-SAKLIESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	333.50	294.00	03/2012 03/2012	03/2013	-	0/0
311	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,577.45	1,708.41	1,418.24	- -	03/2013	-	0/0
312	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,Uttar Pradesh	03/2013	643.00 -	643.00	-	- -	-	-	0/0

Sector Wise Details

(Apr,2013)

S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs crore)	cumulative expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved / Total
						Original	Anticipated		
1	2	3	4	5	6	7	8	9	10
313	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 323.40	750.89	511.30	- -	03/2014	- -	1/1
314	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 155.00	775.36	758.16	- -	10/2012	-	0/0
315	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,041.79	741.88	12/2010 12/2010	03/2015	51(O) 51(R)	0/0
316	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	162.87	108.58	- -	-	-	0/0
317	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Odisha	04/2000	133.41 207.00	276.00	206.41	03/2009 03/2009	08/2014	65(O) 65(R)	0/0
318	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Odisha	04/1994	355.38 470.21	1,995.25	243.58	- -	03/2014	-	0/0
319	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	359.86	1.22	- -	03/2015	-	0/0
320	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36 768.87	768.87	475.10	- 03/2010	03/2010	-	0/0
321	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhand	03/1999	491.19 2,957.21	2,957.21	1,502.86	07/2005 -	-	-	0/0
322	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhand	04/2002	459.91 418.17	418.17	147.37	- -	-	-	0/0
323	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	341.41	287.24	03/2012 03/2013	03/2013	-	0/0
324	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,047.00	1,045.20	9.41	- -	-	-	0/0
325	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	302.23	350.13	- -	12/2012	-	0/0
326	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	223.01	120.74	12/2012 -	03/2015	27(O) -	0/0
327	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	1,630.97	365.82	05/2008 03/2011	-	-	0/0
328	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Odisha	04/1993	100.00 142.98	227.94	221.13	03/2002 -	07/2013	136(O) -	0/0
329	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	4,255.37	3,444.56	03/2009 -	03/2015	72(O) -	0/0
330	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	480.00	0.39	07/2008 -	07/2008	-	0/0
331	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	472.00	168.14	- -	02/2013	-	0/0
332	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 900.05	900.05	677.11	12/2011 12/2011	03/2013	-	0/0
333	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	791.60	0.76	- -	-	-	0/0
334	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	477.88	419.92	03/2012 03/2013	03/2013	-	0/0

Sector Wise Details

(Apr,2013)

S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs crore)	cumulative expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved / Total
						Original / Revised	Anticipated Cost		
1	2	3	4	5	6	7	8	9	10
335	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	1,190.05	304.66	- -	-	-	0/0
336	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	5,300.00	1,247.27	03/2014 03/2016	12/2016	33(O) 9(R)	0/0
337	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	645.00	185.52	- -	03/2012	-	0/0
338	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	883.00	650.87	02/2009 -	03/2012	-	0/0
339	NANGALDAM-TALWARA(NL),NR - [220100188]NR,Multi State	03/1981	37.68 450.00	1,036.78	356.07	07/2012 -	-	-	0/0
340	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	532.87	40.88	- -	-	-	0/0
341	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 200.00	385.20	131.55	- -	03/2015	- -	0/0
342	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 733.00	1,655.81	1,372.73	12/2008 -	03/2015	75(O) -	0/0
343	New BG Rly line from Eklakhi-Balurghat including G - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	703.17	249.01	- -	03/2015	- -	0/0
344	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 850.00	2,446.81	8.45	03/2015 -	03/2017	24(O) -	0/0
345	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 -	2,619.02	286.64	03/2016 -	03/2016	0(O) -	0/0
346	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,069.60	51.45	03/2014 -	03/2014	0(O) -	0/0
347	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	3,951.98	116.43	03/2016 -	03/2016	0(O) -	0/0
348	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	40.92	03/2016 -	06/2016	3(O) -	0/0
349	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	1,117.11	437.69	03/2008 06/2008	-	-	0/0
350	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 380.00	355.00	334.59	03/2009 11/2012	-	-	0/0
351	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 529.23	529.23	249.36	02/2010 11/2012	12/2015	70(O) 37(R)	0/0
352	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 2,921.00	2,921.00	1,751.47	10/2007 12/2012	12/2015	98(O) 36(R)	0/0

Sector Wise Details

(Apr,2013)

S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs crore)	cumulative expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved / Total
						Original / Revised	Anticipated Cost		
1	2	3	4	5	6	7	8	9	10
353	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, Andhra Pradesh	12/1994	124.43 495.68	925.30	604.50	- -	03/2012	-	0/0
354	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER, West Bengal	04/2004	225.68 293.74	293.74	138.09	12/2010 12/2010	12/2010	-	0/0
355	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR, Multi State	03/1998	280.00 842.35	1,029.00	798.85	- -	03/2013	-	0/6
356	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL, Andhra Pradesh	04/2003	136.62 -	289.93	257.91	12/2007 03/2010	-	-	0/0
357	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR, Bihar	04/2002	921.00 2,363.00	2,363.00	1,027.65	03/2009 12/2012	12/2014	69(O) 24(R)	0/0
358	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL, Odisha	04/1999	166.16 -	288.00	271.99	02/2009 02/2009	08/2014	66(O) 66(R)	0/0
359	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]WCR, Madhya pradesh	04/2001	727.13 727.13	1,225.90	225.80	- -	-	-	0/0
360	RANCHI-LOHARDAGA(GC),SER - [220100214]SER, Jharkhand	04/1997	194.07 194.07	596.00	326.81	06/2004 -	12/2012	-	0/0
361	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR, Multi State	01/2004	915.70 915.70	2,232.50	1,787.92	- -	03/2014	-	0/0
362	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER, Odisha	02/1996	57.94 604.04	639.97	175.76	03/1998 08/2005	08/2005	-	0/0
363	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR, Karnataka	04/2007	482.00 482.70	482.70	444.74	03/2013 -	03/2014	12(O) -	0/0
364	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR, Madhya pradesh	04/2008	603.04 603.04	603.04	63.72	03/2012 -	-	-	0/0
365	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL, Chhatisgarh	09/2006	324.90 -	385.54	233.73	03/2010 -	-	-	0/0
366	SEVOK RANGPO, NEFR - [N22000102]NEFR, Sikkim	04/2008	1,339.48 -	3,380.58	58.79	12/2015 -	03/2017	15(O) -	0/0
367	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, Odisha	04/1998	183.23 -	818.29	84.10	02/2015 -	02/2015	0(O) -	0/0
368	Suratpura - Hanumangarh - Sriganganagar Gauge Conv - [N22000114]NWR, Rajasthan	04/2008	516.23 516.23	516.23	175.04	03/2014 -	03/2014	0(O) -	0/0
369	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR, Odisha	04/2005	726.96 810.78	810.78	122.33	- -	-	-	0/0
370	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, West Bengal	03/1984	293.97 1,025.39	1,074.47	439.86	06/2005 07/2011	06/2016	132(O) 59(R)	0/0
371	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, West Bengal	04/2000	157.96 1,188.91	1,188.91	602.44	- 12/2009	02/2012	-	0/0
372	TIDIVANAM-NAGARI (NL) - [N22000085]SR, Tamil Nadu	09/2006	456.00 456.00	582.83	166.81	- -	-	-	0/0
373	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR, Tamil Nadu	09/2006	125.00 125.00	227.40	54.47	- -	-	-	0/0

Sector Wise Details

(Apr,2013)

S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs crore)	cumulative expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved / Total
						Original / Revised	Anticipated Cost		
1	2	3	4	5	6	7	8	9	10
374	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR, Tamil Nadu	09/1995	100.00 100.00	714.05	540.49	- -	-	-	0/0
375	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP, West Bengal	03/2000	907.69 3,156.32	3,176.10	3,421.35	12/2006 08/2010	08/2010	-	0/0
376	Tinpahar - Sahibganj (ER) - [N22000115]ER, Jharkhand	04/2008	167.73 167.73	167.73	65.64	03/2012 -	02/2013	-	0/0
377	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, Jammu and Kashmir	03/1995	2,500.00 2,500.00	20,000.00	8,877.37	03/2001 -	12/2017	201(O) -	0/0
378	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR, Uttar Pradesh	04/2006	325.00 325.00	819.40	198.24	03/2010 03/2017	03/2017	84(O) 0(R)	0/0
379	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR, Gujarat	04/2008	1,389.62 -	1,389.62	289.39	03/2014 -	03/2014	0(O) -	0/0
380	VIRAMGAM-BHILDI(WR), GC - [220100062]WR, Multi State	04/1990	155.66 356.87	356.87	160.73	- 03/2010	-	-	0/0
	Total		66,990.82 -	155,817.76	62,346.40				1/7
Road Transport & Highways									
381	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI, Uttar Pradesh	10/2012	250.50 -	250.50	84.88	10/2014 -	10/2014	0(O) -	0/0
382	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI, Uttar Pradesh	01/2013	373.47 -	373.47	38.08	07/2014 -	07/2014	0(O) -	0/0
383	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, Bihar	05/2011	351.54 -	351.54	392.02	05/2013 -	03/2014	10(O) -	0/0
384	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI, Bihar	05/2011	511.54 -	511.54	579.51	11/2013 -	11/2013	0(O) -	0/0
385	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI, Multi State	04/2012	624.00 -	624.00	148.73	04/2014 -	04/2014	0(O) -	0/0
386	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI, Bihar	07/2012	356.40 -	356.40	-	07/2014 -	07/2014	0(O) -	0/0
387	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, Uttar Pradesh	07/2012	291.36 -	291.36	55.19	01/2014 -	01/2014	0(O) -	0/0
388	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI, Meghalaya	02/2011	226.00 -	226.00	129.80	02/2014 -	02/2014	0(O) -	0/0
389	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, Bihar	05/2011	664.00 -	664.00	427.14	02/2014 -	04/2014	2(O) -	0/0
390	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, Bihar	10/2011	375.09 -	375.09	174.37	04/2014 -	04/2014	0(O) -	0/0
391	2laning with PS Gopalganj-Chappra - [N24000190]NHAI, Bihar	12/2011	325.00 -	325.00	160.69	05/2014 -	05/2014	0(O) -	0/0
392	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI, Multi State	02/2011	2,498.76 -	2,498.76	1,718.30	08/2014 -	07/2015	11(O) -	0/0

Sector Wise Details

(Apr,2013)

S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs crore)	cumulative expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved / Total
						Original	Anticipated		
1	2	3	4	5	6	7	8	9	10
393	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50	1,008.50	1,242.30	06/2013	06/2013	0(O)	0/0
394	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00	359.00	38.55	09/2013	07/2014	10(O)	0/0
395	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI, Gujarat	03/2011	785.50	785.50	776.33	08/2013	08/2013	0(O)	0/0
396	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,Bihar	01/2011	575.00	575.00	293.00	07/2013	07/2013	0(O)	0/0
397	4-laning of Barhi-Hazaribagh - [N24000191]NHAI,Jharkhand	02/2012	398.00	398.00	424.27	02/2014	02/2014	0(O)	0/0
398	4-laning of Brahmapore-Faraka - [N24000203]NHAI,Multi State	02/2011	998.79	998.79	1,034.80	08/2013	08/2013	0(O)	0/0
399	4-laning of Faraka-Raiganj - [N24000202]NHAI,Multi State	02/2011	1,078.84	1,078.84	1,108.40	08/2013	08/2013	0(O)	0/0
400	4-laning of Raiganj-Dalkola - [N24000204]NHAI,Multi State	02/2011	580.43	580.43	218.49	08/2013	08/2013	0(O)	0/0
401	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,West Bengal	04/2012	1,396.18	1,396.18	686.56	09/2014	09/2014	0(O)	0/0
402	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16	465.50	218.43	09/2007	03/2014	78(O)	0/0
403	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,Gujarat	01/2013	2,125.24	2,125.24	30.19	12/2015	12/2015	0(O)	0/0
404	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00	705.00	1,255.60	11/2012	06/2013	7(O)	0/0
405	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00	190.00	264.27	01/2009	12/2013	59(O)	0/0
406	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56	390.56	772.27	02/2012	06/2013	16(O)	0/0
407	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Odisha	04/2000	228.70	228.70	194.51	02/2004	05/2013	111(O)	0/0
408	BAREILY-SITAPUR - [N24000200]NHAI,Uttar Pradesh	03/2011	1,046.00	1,046.00	303.63	09/2013	09/2013	0(O)	0/0
409	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,Rajasthan	12/2011	2,388.00	2,388.00	1,025.20	06/2014	06/2014	0(O)	0/0
410	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka	12/2010	480.00	480.00	488.69	-	10/2013	-	2/2
411	BHOPAL-SANCHI - [N24000192]NHAI,Madhya pradesh	10/2011	209.00	209.00	13.80	01/2013	10/2013	9(O)	0/0
412	BHUBANESWAR TO PURI - [N24000195]NHAI,Odisha	03/2011	500.29	500.29	450.94	08/2013	08/2013	0(O)	0/0
413	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80	237.80	277.43	06/2008	03/2014	69(O)	0/0
414	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00	195.00	232.51	06/2008	03/2014	69(O)	0/0

Sector Wise Details

(Apr,2013)

S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs crore)	cumulative expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved / Total
						Original	Anticipated		
1	2	3	4	5	6	7	8	9	10
415	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00	230.00	233.72	06/2005	03/2014	105(O)	0/0
416	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61	217.61	258.43	04/2010	11/2014	55(O)	0/0
417	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00	281.31	179.23	02/2010	07/2014	53(O)	0/0
418	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, Tamil Nadu	09/2010	852.00	852.00	797.24	03/2013	08/2013	5(O)	0/0
419	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI, Karnataka	03/2011	839.00	839.00	570.06	-	12/2013	-	0/1
420	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00	1,585.00	957.76	05/2013	09/2013	4(O)	0/0
421	Chennai-Tada(Six lane) - [N24000129]NHAI, Tamil Nadu	04/2009	353.37	353.37	395.08	10/2011	03/2014	29(O)	0/0
422	Chikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30	572.30	765.86	10/2011	06/2013	20(O)	0/0
423	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI, Bihar	12/2003	300.00	300.00	176.84	10/2008	06/2014	68(O)	0/0
424	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,Multi State	10/2012	1,928.22	1,928.22	302.56	04/2015	04/2015	0(O)	0/0
425	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00	486.00	644.73	05/2010	06/2013	37(O)	0/0
426	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	593.00	593.00	503.38	07/2013	07/2013	0(O)	0/0
427	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI, Tamil Nadu	06/2011	600.00	600.00	75.85	06/2013	06/2013	0(O)	0/0
428	DEVIHALLI-HASSAN - [N24000152]NHAI, Karnataka	12/2010	453.00	453.00	524.25	-	06/2013	-	1/1
429	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI, Assam	12/2003	200.00	200.00	246.20	06/2008	05/2013	59(O)	0/0
430	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00	160.00	197.55	05/2008	12/2013	67(O)	0/0
431	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45	232.45	295.39	09/2010	01/2014	40(O)	0/0
432	Dindigul - Kumli - [N24000177]NHAI, Tamil Nadu	09/2011	485.00	485.00	303.41	08/2013	02/2015	18(O)	0/0
433	ETAWAH CHAKERI - [N24000219]NHAI, Uttar Pradesh	03/2013	1,573.00	1,573.00	13.39	09/2015	09/2015	0(O)	0/0
434	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI, Bihar	12/2003	332.94	332.94	441.45	09/2008	05/2013	56(O)	0/0
435	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,Multi State	02/2013	1,232.00	1,232.00	108.59	08/2015	08/2015	0(O)	0/0

Sector Wise Details

(Apr,2013)

S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs crore)	cumulative expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved / Total
						Original / Revised	Anticipated Cost		
1	2	3	4	5	6	7	8	9	10
436	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,Kerala	04/2011	682.00	682.00	-	10/2013	03/2014	5(O)	0/0
437	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52	1,170.52	4.41	06/2011	12/2013	30(O)	0/0
438	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00	201.66	142.58	09/2008	03/2014	66(O)	0/0
439	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Odisha	04/2000	263.27	263.27	276.26	02/2004	05/2013	111(O)	0/0
440	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00	1,141.00	1,200.30	08/2013	08/2013	0(O)	0/0
441	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16	198.16	242.38	04/2008	03/2014	71(O)	0/0
442	GUWAHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96	175.96	182.53	04/2008	03/2014	71(O)	0/0
443	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya Pradesh	12/2003	300.93	300.93	303.02	10/2009	05/2013	43(O)	0/0
444	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00	604.00	495.37	12/2009	07/2013	43(O)	0/0
445	Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10	1,509.10	1,675.00	09/2012	12/2013	15(O)	0/0
446	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70	1,673.70	2,777.00	10/2011	12/2013	26(O)	0/0
447	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00	220.00	284.17	09/2007	11/2013	74(O)	0/0
448	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00	280.00	303.32	02/2009 03/2014	05/2014	63(O) 2(R)	0/0
449	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00	363.74	132.67	07/2009	05/2014	58(O)	0/0
450	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00	386.10	59.89	09/2007	04/2014	79(O)	0/0
451	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,Uttarakhand	11/2011	478.00	478.00	245.42	10/2013	03/2014	5(O)	0/0
452	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00	207.56	192.39	08/2004	06/2013	106(O)	0/0
453	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00	196.65	192.06	08/2004 07/2010	06/2013	106(O) 35(R)	0/0
454	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhand	08/2010	625.07	625.07	943.25	01/2013	06/2013	5(O)	0/0
455	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI,Karnataka	09/2010	946.00	946.00	1,485.60	-	06/2013	-	3/3

Sector Wise Details

(Apr,2013)

S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs crore)	cumm expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved / Total
						Original / Revised	Anticipated Cost		
1	2	3	4	5	6	7	8	9	10
456	INDORE-DEWAS(NH-3) - [N24000159]NHAI, Madhya pradesh	11/2010	325.00	325.00	447.50	05/2013	02/2014	9(O)	0/0
457	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI, Madhya pradesh	10/2010	1,175.00	1,175.00	138.67	04/2013	04/2013	0(O)	0/0
458	JAIPUR-REENGUS - [N24000198]NHAI, Rajasthan	08/2010	267.81	267.81	630.65	02/2013	07/2013	5(O)	0/0
459	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, Jammu and Kashmir	07/2010	1,813.76	1,813.76	-	07/2013	06/2014	11(O)	0/0
460	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI, Uttar Pradesh	12/2003	355.06	355.06	501.86	09/2009	06/2013	45(O)	0/0
461	JORBAT - BARAPANI - [N24000180]NHAI, Meghalaya	01/2011	536.00	536.00	333.90	01/2014	01/2014	0(O)	0/0
462	Jaipur-Tonk-Deoli - [N24000135]NHAI, Rajasthan	06/2010	792.06	792.06	1,933.70	12/2012	06/2013	6(O)	0/0
463	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI, Rajasthan	12/2003	275.00	250.39	279.83	10/2008	09/2013	59(O)	0/0
464	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00	240.00	295.65	10/2008	12/2013	62(O)	0/0
465	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, West Bengal	02/2012	702.16	702.16	411.22	07/2014	07/2014	0(O)	0/0
466	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI, Karnataka	09/2010	671.00	671.00	737.54	-	06/2014	-	2/3
467	Kishangarh-Ajmer-Beawer - [N24000128]NHAI, Rajasthan	11/2009	795.00	795.00	1,055.70	05/2012	06/2013	13(O)	0/0
468	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI, Madhya pradesh	12/2003	407.60	407.60	186.40	06/2010	12/2013	42(O)	0/0
469	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI, Madhya pradesh	12/2003	263.17	263.17	233.77	09/2009	09/2014	60(O)	0/0
470	LUCKNOW-RAIBAREILI - [N24000207]NHAI, Uttar Pradesh	07/1999	635.90	635.90	-	07/2012	07/2014	24(O)	0/0
471	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, Assam	12/2003	155.04	280.13	114.81	11/2008	06/2014	67(O)	0/0
472	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, Assam	12/2003	199.81	385.13	83.98	04/2009	12/2014	68(O)	0/0
473	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, Assam	12/2003	167.64	167.64	45.43	11/2008	12/2014	73(O)	0/0
474	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, Assam	12/2003	200.00	200.00	141.82	04/2009	12/2014	68(O)	0/0
475	MURADABAD-BAREILLY - [N24000154]NHAI, Uttar Pradesh	04/2010	1,267.00	1,267.00	1,430.60	06/2013	06/2013	0(O)	0/0

Sector Wise Details

(Apr,2013)

S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs crore)	cumm expenditure	Date of Commissioning		Delay w.r.t. Original /Revised (in months)	Milestones Achieved / Total
						Original / Revised	Anticipated Cost		
1	2	3	4	5	6	7	8	9	10
476	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, Multi State	09/2011	754.00	754.00	512.09	03/2013	03/2014	12(O)	0/0
477	Muzafarpur - Sonbarsa - [N24000174]NHAI, Bihar	05/2011	511.54	511.54	65.78	11/2013	11/2013	0(O)	0/0
478	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, Assam	12/2003	264.72	264.72	299.20	06/2008	05/2013	59(O)	0/0
479	NAGPUR-KONDHALI, NH-6(NHAI) - [N24000055]NHAI, Maharashtra	03/2005	168.00	168.00	457.30	12/2008	06/2013	54(O)	0/0
480	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI, Maharashtra	04/2012	484.19	484.19	34.07	10/2014	10/2014	0(O)	0/0
481	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00	208.00	290.59	04/2008	05/2014	73(O)	0/0
482	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, Assam	12/2003	225.00	225.00	258.39	06/2008	09/2013	63(O)	0/0
483	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00	200.00	282.24	06/2008	09/2013	63(O)	0/0
484	NASHRI CHANANI - [N24000162]NHAI, Jammu and Kashmir	06/2010	2,159.00	2,159.00	-	06/2015	05/2016	11(O)	0/0
485	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI, Karnataka	04/2000	196.50	196.50	268.59	06/2011	06/2013	24(O)	0/2
486	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, Kerala	03/2005	557.00	557.00	932.27	02/2010	12/2014	58(O)	0/0
487	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI, Odisha	07/2011	586.00	586.00	237.55	01/2014	01/2014	0(O)	0/0
488	New 4 Lane elevated road from chennai airport - [N24000139]NHAI, Tamil Nadu	09/2010	1,655.00	1,655.00	393.70	09/2013	09/2013	0(O)	0/0
489	ORAI TO JHANSI (UP-5), NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI, Uttar Pradesh	12/2003	340.68	340.68	400.56	03/2008	05/2013	62(O)	0/0
490	PANIKHOLI-RIMOLI - [N24000197]NHAI, Odisha	03/2012	1,410.00	1,410.00	78.55	09/2014	09/2014	0(O)	0/0
491	PANIPAT-ROHTAK - [N24000151]NHAI, Haryana	04/2011	807.00	807.00	1,239.30	10/2014	10/2014	0(O)	0/0
492	PANVEL-INDAPUR - [N24000216]NHAI, Multi State	12/2011	942.69	942.69	128.49	06/2014	06/2014	0(O)	0/0
493	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI, Punjab	12/2003	284.00	359.00	284.54	05/2008	09/2013	64(O)	0/0
494	PATNA-BAKTARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, Bihar	09/2011	574.00	574.00	58.67	03/2014	03/2014	0(O)	0/0
495	PATNA-MUZAFFARPUR - [N24000165]NHAI, Bihar	08/2010	671.30	671.30	603.09	02/2013	10/2013	8(O)	0/0
496	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, Maharashtra	03/2005	940.00	940.00	1,293.20	07/2012	06/2013	11(O)	0/0
497	PUNE-SATARA(NH-4) - [N24000156]NHAI, Maharashtra	10/2010	1,724.55	1,724.55	1,127.30	03/2013	04/2014	13(O)	0/0
498	PUNE-SHOLAPUR, Pkg-II - [N24000193]NHAI, Maharashtra	09/2011	835.00	835.00	122.65	01/2014	01/2014	0(O)	0/0

Sector Wise Details

(Apr,2013)

S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs crore)	cumm expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved / Total
						Original / Revised	Anticipated Cost		
1	2	3	4	5	6	7	8	9	10
499	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00	2,288.00	3,465.90	11/2011	08/2013	21(O)	0/0
500	Pune-sholapur, pkg1 - [N24000127]NHAI, Maharashtra	11/2009	1,110.00	1,110.00	1,802.10	05/2012	10/2013	17(O)	0/0
501	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,Jammu and Kashmir	07/2010	1,987.00	1,987.00	765.69	07/2015	06/2016	11(O)	0/0
502	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, Madhya pradesh	12/2003	251.03	251.03	326.46	10/2008	06/2013	56(O)	0/0
503	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI, Multi State	12/2012	1,479.00	1,479.00	162.83	06/2015	06/2015	0(O)	0/0
504	ROHTAK-BAWAL - [N24000169]NHAI, Haryana	05/2011	650.00	650.00	1,024.10	11/2013	11/2013	0(O)	0/0
505	SALEM - U / UNDRUPET (BOT -1/TN-06) NH -68 - [N24000102]NHAI, Tamil Nadu	03/2005	941.00	941.00	1,901.00	01/2011	05/2013	28(O)	0/0
506	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI, Gujarat	09/2010	805.39	805.39	209.80	03/2013	12/2013	9(O)	0/0
507	SAMAIKHALI GANDHIDHAM - [N24000223]NHAI, Gujarat	09/2010	805.39	805.39	543.71	12/2013	12/2013	0(O)	0/0
508	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI, Odisha	11/2011	909.00	909.00	844.05	05/2014	05/2014	0(O)	0/0
509	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, Assam	12/2003	157.47	154.57	231.80	09/2007	12/2013	75(O)	0/0
510	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, West Bengal	12/2003	225.00	225.00	190.95	07/2008	03/2013	-	0/0
511	SIX LANNING OF HOSUR-KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI, Tamil Nadu	06/2011	535.00	535.00	-	12/2013	12/2013	0(O)	0/0
512	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM. - [N24000172]NHAI, Tamil Nadu	09/2011	1,250.00	1,250.00	14.58	12/2013	12/2013	0(O)	0/0
513	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI, Andhra Pradesh	11/2011	1,535.00	1,535.00	822.95	05/2014	05/2014	0(O)	0/0
514	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI, Kerala	02/2010	617.00	617.00	154.52	08/2012	03/2015	31(O)	0/0
515	SNG toBANL - [N24000189]NHAI, Jammu and Kashmir	06/2011	1,100.70	1,100.70	-	06/2014	06/2014	0(O)	0/0
516	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, Assam	12/2003	245.00	245.00	491.21	03/2008	06/2013	63(O)	0/0
517	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI, Odisha	04/2000	225.00	241.53	161.44	04/2004	05/2013	109(O)	0/0
518	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI, Multi State	02/2009	1,693.75	1,693.75	2,686.20	08/2011	06/2013	22(O)	0/0

Sector Wise Details

(Apr,2013)

S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs crore)	cumulative expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved / Total
						Original / Revised	Anticipated Cost		
1	2	3	4	5	6	7	8	9	10
519	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00	280.00	581.49	06/2009	06/2013	48(O)	0/0
520	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00	516.00	853.94	07/2010	03/2014	44(O)	0/0
521	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00	567.00	891.08	11/2013	11/2013	0(O)	0/0
522	Tirupati - Chennai - [N24000178]NHAI,Tamil Nadu	04/2011	571.00	571.00	-	10/2013	10/2013	0(O)	0/0
523	Trichy Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00	374.00	101.30	05/2013	05/2013	0(O)	0/0
524	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00	680.00	-	-	04/2013	-	2/2
525	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,Multi State	09/2011	2,848.00	2,848.00	787.97	03/2014	03/2014	0(O)	0/0
526	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,Jammu and Kashmir	12/2003	166.27	193.10	193.46	03/2008	03/2013	-	0/0
527	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45	193.45	47.41	11/2012	03/2014	16(O)	0/0
528	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88	953.88	585.12	07/2013	06/2014	11(O)	0/0
529	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]NHAI,Multi State	12/2011	1,047.00	1,047.00	201.61	06/2014	06/2014	0(O)	0/0
Total			101,529.76	103,468.38	72,801.29				10/14
Shipping & Ports									
530	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44	359.44	358.78	04/2011	09/2013	29(O)	0/0
531	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,Multi State	07/2011	220.49	220.49	98.31	01/2013	06/2013	5(O)	0/0
532	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPL - [N25000062]SHIPP.,Multi State	01/2012	511.87	511.87	106.72	03/2014	08/2014	5(O)	0/0
533	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72	532.83	364.52	12/2012	10/2013	10(O)	0/0
534	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03	277.03	294.87	12/2011	10/2012	-	0/0
535	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46	994.82	306.12	02/2014	02/2014	0(O)	0/0
536	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10	1,012.23	554.60	12/2013	11/2013	-1(O)	0/0

Sector Wise Details

(Apr,2013)

S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs crore)	cumulative expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved / Total
						Original / Revised	Anticipated Cost		
1	2	3	4	5	6	7	8	9	10
537	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	946.21	12/2010 09/2012	04/2014	40(O) 19(R)	0/0
538	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	-	0/0
539	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012	-	0/0
540	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 1,571.60	1,571.60	5.75	10/2008 -	10/2008	-	0/0
541	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Odisha	12/2005	154.84 -	253.36	-	- 01/2009	01/2009	-	0/1
542	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 309.00	600.00	139.80	03/2006 06/2013	06/2013	87(O) 0(R)	0/0
543	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	-	0/0
544	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	277.00	0.21	03/2012 -	03/2012	-	0/0
545	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	373.22	371.18	04/2009 11/2009	02/2011	-	0/0
546	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	2,427.40	831.23	10/2008 11/2010	-	-	0/0
547	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	4,150.00	3,661.95	01/2012 09/2012	07/2013	18(O) 10(R)	0/0
548	Setting up of Single Point Mooring (SPM) and allie - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -	621.53	-	05/2013 -	05/2013	0(O) -	0/0
Total			15,617.12 -	17,902.42	8,260.18				0/1
Telecommunications									
549	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	164.18	01/2009 -	08/2013	55(O) -	0/0
550	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	247.00	75.89	02/2007 -	-	-	0/0
551	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 -	229.41	67.20	02/2007 03/2012	02/2013	-	0/0

Sector Wise Details

(Apr,2013)

S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs crore)	cum expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved / Total
						Original / Revised	Anticipated Cost		
1	2	3	4	5	6	7	8	9	10
552	DELHI CONVERGENT BILLING AND CRM PE-5834 - [N26000099]MTNL,Delhi	02/2006	229.41	229.41	-	03/2012	-	-	0/0
553	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00	384.00	29.45	10/2010 03/2012	12/2013	38(O) 21(R)	0/0
554	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]MTNL,Maharashtra	06/2006	231.38	168.30	86.11	10/2007	-	-	0/0
555	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttarakhand	01/2009	149.15	158.72	80.05	06/2009	08/2013	50(O) -	0/0
556	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94	373.94	227.58	12/2008	12/2012	-	0/0
557	GSM equipment of 1625000Lines (2G) 325000 lines 3(-) [N26000090]BSNL,Madhya pradesh	11/2009	916.70	916.70	828.48	11/2010 12/2012	06/2013	31(O) 6(R)	0/0
558	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhand	03/2008	328.13	392.13	164.58	03/2009	01/2013	-	0/0
559	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65	152.65	-	03/2010	-	-	0/0
560	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88	952.88	-	03/2010	-	-	0/0
561	Supply Installation testing and commissioning of Rural Wimax - [N26000100]BSNL,Multi State	07/2010	1,148.19	964.37	178.11	05/2011	08/2013	27(O) -	0/0
Total			5,699.24	5,506.32	1,901.63				0/0
Urban Development									
562	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00	11,609.00	2,482.18	06/2011	03/2013	-	3/3
563	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	173.08	-	04/2009	-	-	0/0
564	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00	35,242.00	2,931.13	03/2016	03/2016	0(O) -	0/0
565	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00	2,494.00	258.11	09/2014	09/2014	0(O) -	0/0
Total			44,245.18	49,518.08	5,671.42				3/3
Water Resources									
566	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90	1,187.00	35.49	12/2007	12/2012	-	0/0

Sector Wise Details

(Apr,2013)

						Date of Commissioning		Delay w.r.t. Original /Revised (in months)	Milestones Achieved/ Total
S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs crore)	cumm expenditure	Original / Revised	Anticipated Cost		
1	2	3	4	5	6	7	8	9	10
	Total		542.90	1,187.00	35.49				0/0
			-						
Grand Total			798,047.83	943,167.88	456,277.05				1067/3446

Sector wise current status of projects on the Flash Report

Urban Development


I. Current Status:

Number of Projects	4
Number of Projects On Schedule	2

Number of Projects Without Date Of Commissioning	2
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 2 projects are on schedule and 2 projects do not have fixed dates of commissioning.

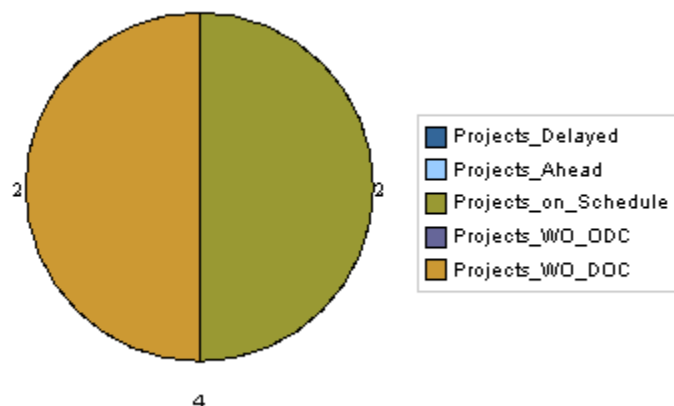

III. Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 44245.18 crore but this was subsequently revised to Rs. 49518.08 crore implying a cost overrun of 11.9%. The expenditure incurred on these projects till April, 2013 is Rs. 5671.42 crore, which is 11.5% of the revised cost of the projects.

Figures are in Rs. Crore

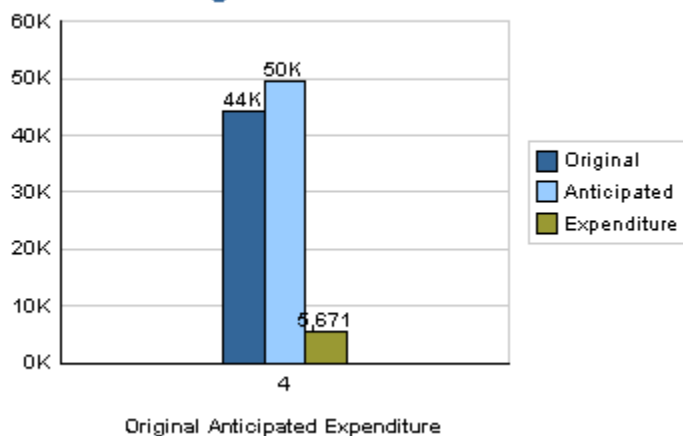

Sector wise current status of projects on the Flash Report

Telecommunications

I. Current Status:


Number of Projects **13**

Number of Projects Delayed **5**

Number of Projects Without Date Of Commissioning **8**

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 13 projects, 5 projects are delayed .8 projects do not have fixed dates of commissioning.

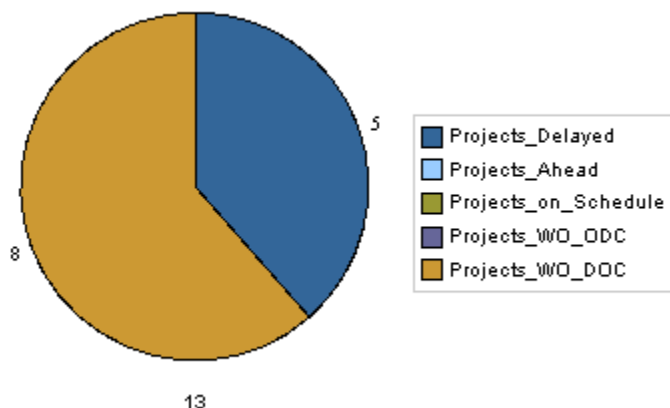

III. Investment Scenario

The Total Original cost of implementation of 13 projects when sanctioned, was of the order of Rs. 5699.24 crore but this was subsequently revised to Rs. 5506.32 crore implying a cost overrun of -3.4%. The expenditure incurred on these projects till April, 2013 is Rs. 1901.63 crore, which is 34.5% of the revised cost of the projects.

Figures are in Rs. Crore

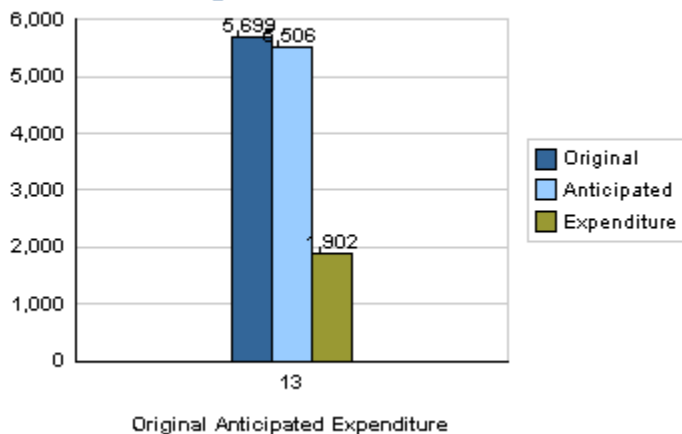

Sector wise current status of projects on the Flash Report


Shipping & Ports

I. Current Status:

Number of Projects	19
Number of Projects On Schedule	2
Number of Projects Delayed	7
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	9

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 19 projects, 1 project are ahead of schedule, 2 projects are on schedule and 7 projects are delayed .9 projects do not have fixed dates of commissioning.

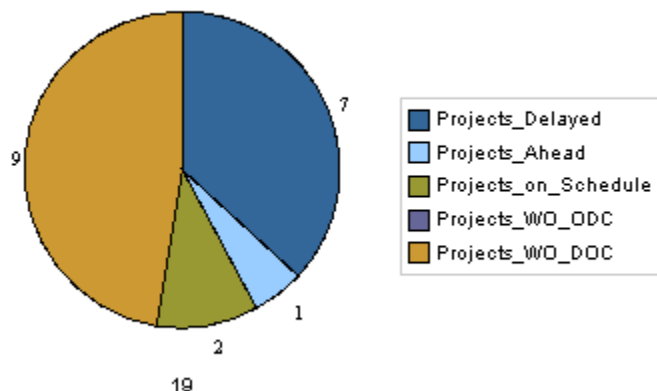

III. Investment Scenario

The Total Original cost of implementation of 19 projects when sanctioned, was of the order of Rs. 15617.12 crore but this was subsequently revised to Rs. 17902.42 crore implying a cost overrun of 14.6%. The expenditure incurred on these projects till April, 2013 is Rs. 8260.18 crore, which is 46.1% of the revised cost of the projects.

Figures are in Rs. Crore

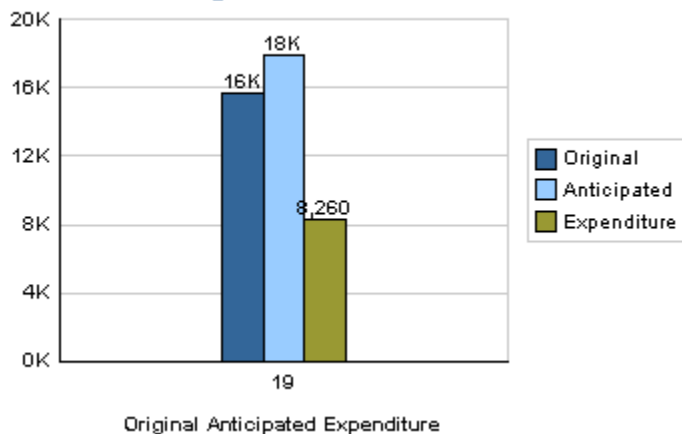

Sector wise current status of projects on the Flash Report

Road Transport & Highways


I. Current Status:

Number of Projects	149
Number of Projects On Schedule	53
Number of Projects Delayed	88

Number of Projects Without Original Date of Commissioning	6
Number of Projects Without Date Of Commissioning	2


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 149 projects, 53 projects are on schedule and 88 projects are delayed .2 projects do not have fixed dates of commissioning.6 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

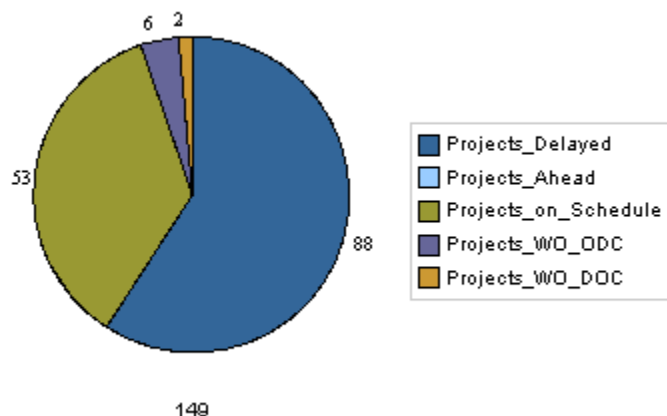

III. Investment Scenario

The Total Original cost of implementation of 149 projects when sanctioned, was of the order of Rs. 101529.76 crore but this was subsequently revised to Rs. 103468.38 crore implying a cost overrun of 1.9%. The expenditure incurred on these projects till April, 2013 is Rs. 72801.29 crore, which is 70.4% of the revised cost of the projects.

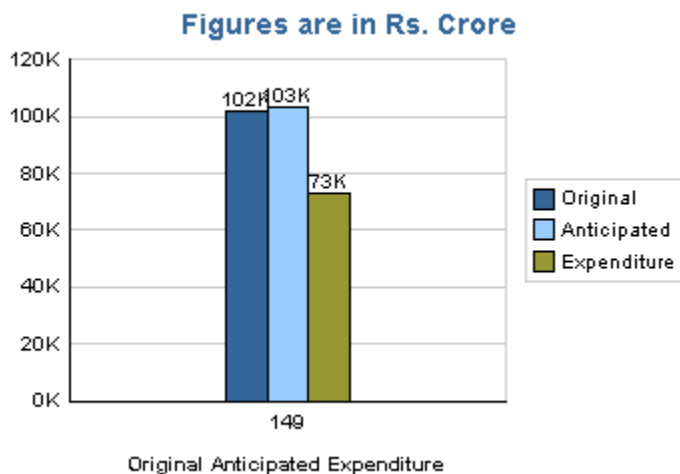

Sector wise current status of projects on the Flash Report

Railways


I. Current Status:

Number of Projects	129
Number of Projects On Schedule	9
Number of Projects Delayed	33

Number of Projects Without Original Date of Commissioning	9
Number of Projects Without Date Of Commissioning	78

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 129 projects, 9 projects are on schedule and 33 projects are delayed .78 projects do not have fixed dates of commissioning.9 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

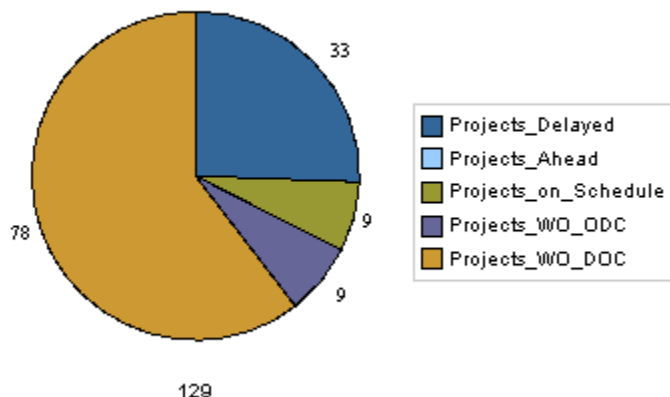

III. Investment Scenario

The Total Original cost of implementation of 129 projects when sanctioned, was of the order of Rs. 66990.82 crore but this was subsequently revised to Rs. 155817.76 crore implying a cost overrun of 132.6%. The expenditure incurred on these projects till April, 2013 is Rs. 62346.4 crore, which is 40% of the revised cost of the projects.

Figures are in Rs. Crore

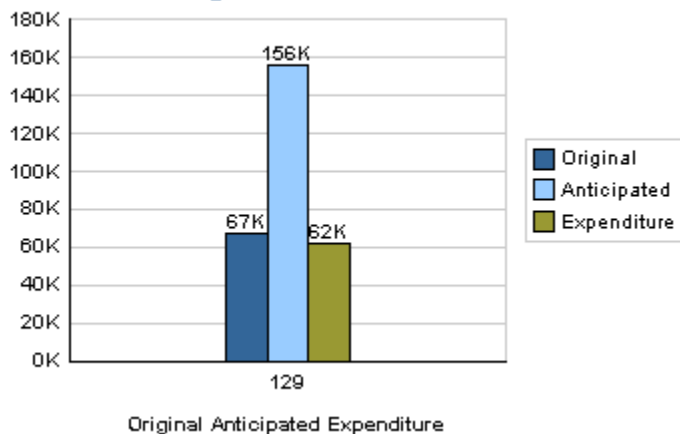

Sector wise current status of projects on the Flash Report


Power

I. Current Status:

Number of Projects	100
Number of Projects On Schedule	40
Number of Projects Delayed	51
Number of Projects Ahead	2
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	6


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 100 projects, 2 projects are ahead of schedule, 40 projects are on schedule and 51 projects are delayed .6 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

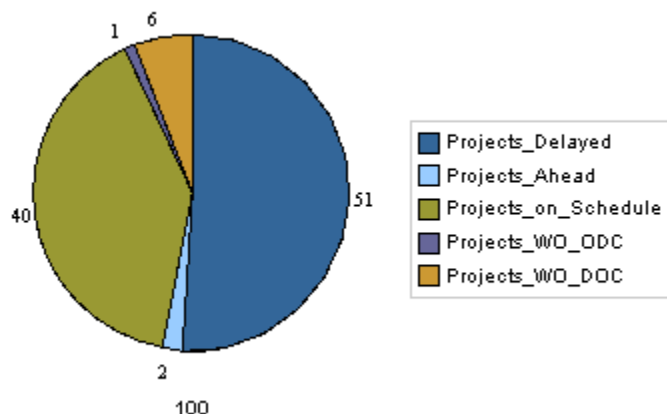

III. Investment Scenario

The Total Original cost of implementation of 100 projects when sanctioned, was of the order of Rs. 242845 crore but this was subsequently revised to Rs. 258586.29 crore implying a cost overrun of 6.5%. The expenditure incurred on these projects till April, 2013 is Rs. 122369.06 crore, which is 47.3% of the revised cost of the projects.

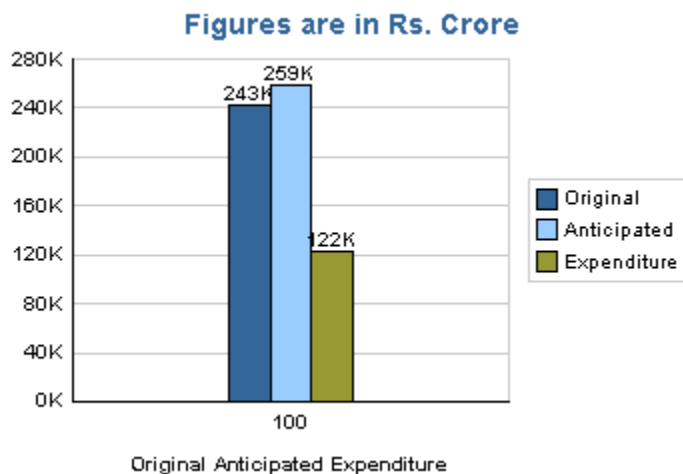

Sector wise current status of projects on the Flash Report

Petroleum


I. Current Status:

Number of Projects	70
Number of Projects On Schedule	20
Number of Projects Delayed	40

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	9


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 70 projects, 20 projects are on schedule and 40 projects are delayed .9 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

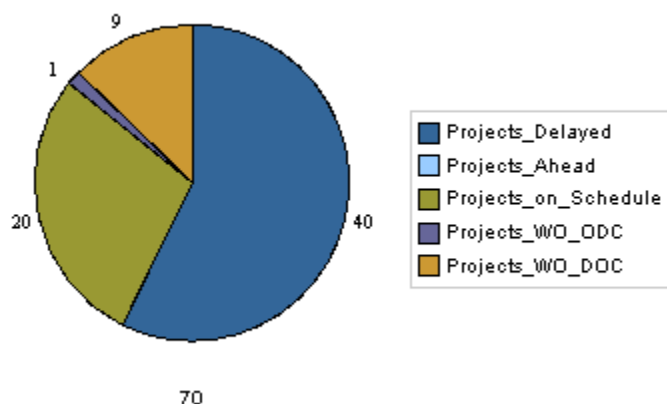

III. Investment Scenario

The Total Original cost of implementation of 70 projects when sanctioned, was of the order of Rs. 165950.52 crore but this was subsequently revised to Rs. 178609.86 crore implying a cost overrun of 7.6%. The expenditure incurred on these projects till April, 2013 is Rs. 83622.41 crore, which is 46.8% of the revised cost of the projects.

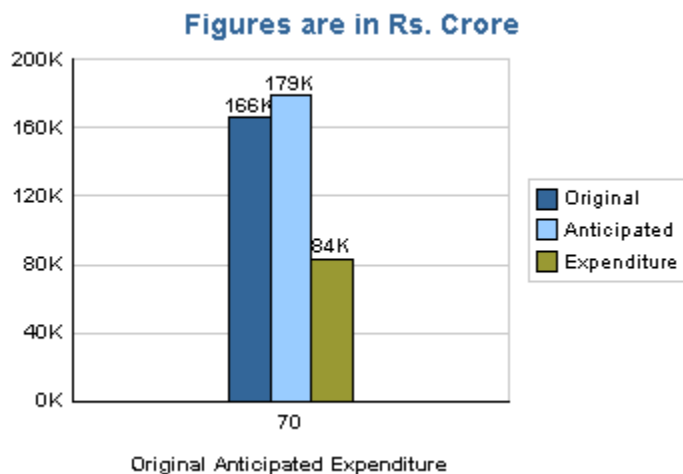

Sector wise current status of projects on the Flash Report


Steel

I. Current Status:

Number of Projects	17
Number of Projects On Schedule	2
Number of Projects Delayed	15

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 17 projects, 2 projects are on schedule and 15 projects are delayed.

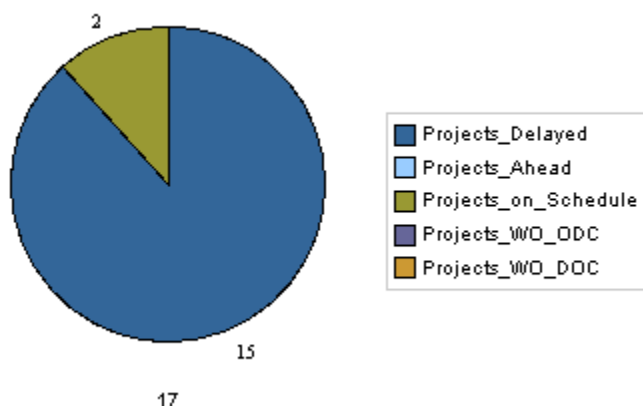

III. Investment Scenario

The Total Original cost of implementation of 17 projects when sanctioned, was of the order of Rs. 65285.87 crore but this was subsequently revised to Rs. 71443.41 crore implying a cost overrun of 9.4%. The expenditure incurred on these projects till April, 2013 is Rs. 48647.59 crore, which is 68.1% of the revised cost of the projects.

Figures are in Rs. Crore

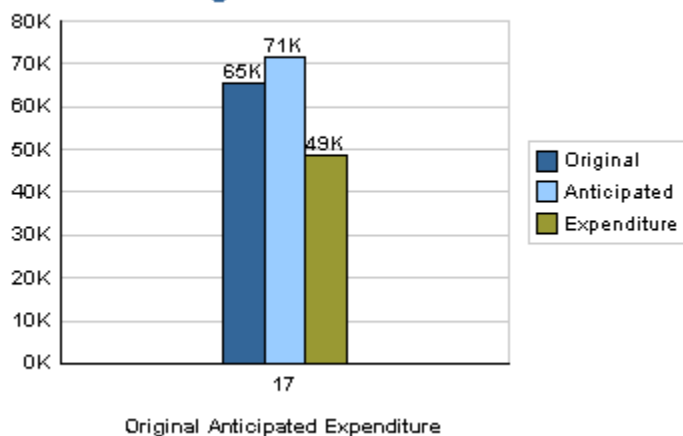

Sector wise current status of projects on the Flash Report

Coal


I. Current Status:

Number of Projects	52
Number of Projects On Schedule	19
Number of Projects Delayed	29

Number of Projects Without Date Of Commissioning 4


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 52 projects, 19 projects are on schedule and 29 projects are delayed .4 projects do not have fixed dates of commissioning.

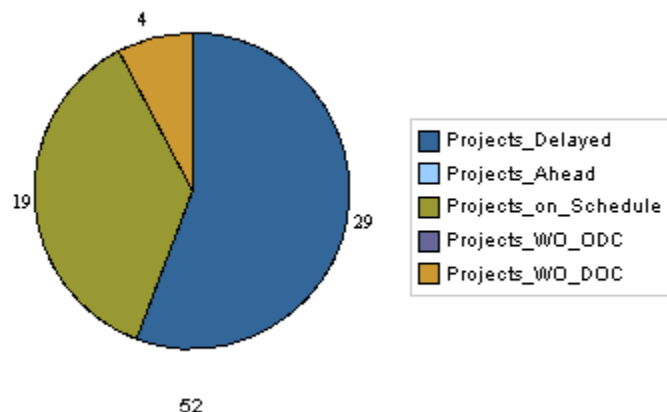

III. Investment Scenario

The Total Original cost of implementation of 52 projects when sanctioned, was of the order of Rs. 36486.6 crore but this was subsequently revised to Rs. 37940.66 crore implying a cost overrun of 4%. The expenditure incurred on these projects till April, 2013 is Rs. 14957.41 crore, which is 39.4% of the revised cost of the projects.

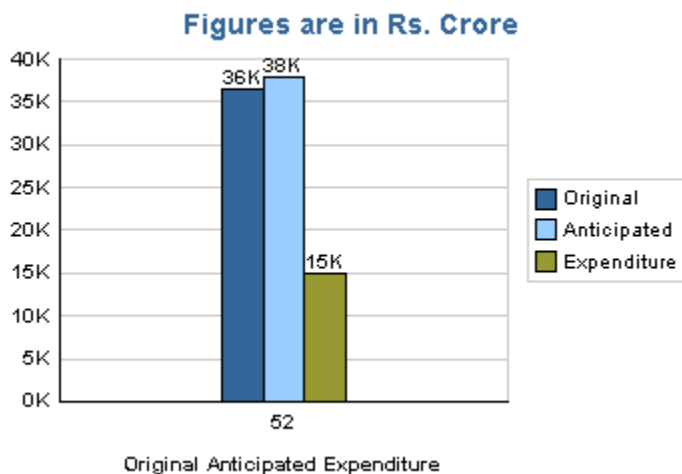

Sector wise current status of projects on the Flash Report

Civil Aviation


I. Current Status:

Number of Projects	6
Number of Projects On Schedule	2
Number of Projects Delayed	2

Number of Projects Without Date Of Commissioning	2
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 6 projects, 2 projects are on schedule and 2 projects are delayed .2 projects do not have fixed dates of commissioning.

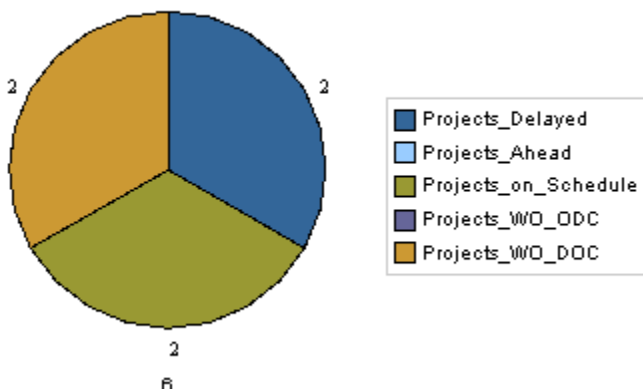

III. Investment Scenario

The Total Original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 5473.58 crore but this was subsequently revised to Rs. 6063.07 crore implying a cost overrun of 10.8%. The expenditure incurred on these projects till April, 2013 is Rs. 5271.18 crore, which is 86.9% of the revised cost of the projects.

Figures are in Rs. Crore

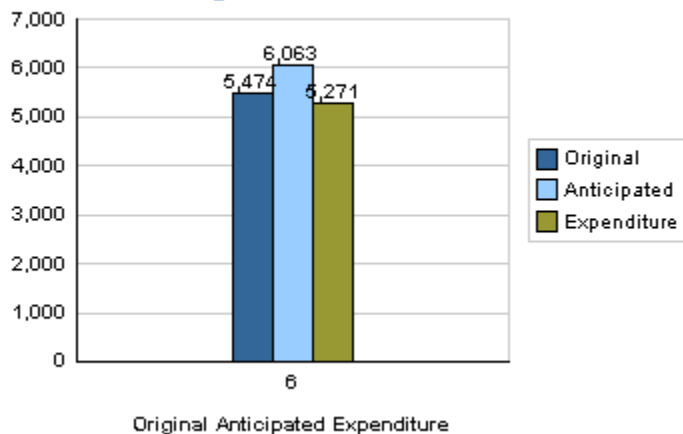

Sector wise current status of projects on the Flash Report

Atomic Energy

I. Current Status:


Number of Projects 4

Number of Projects Delayed 2

Number of Projects Without Date Of Commissioning 2

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 2 projects are delayed .2 projects do not have fixed dates of commissioning.

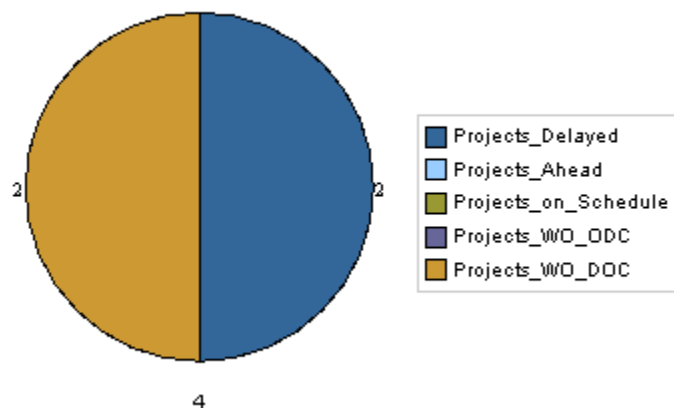

III. Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 40442 crore but this was subsequently revised to Rs. 46726 crore implying a cost overrun of 15.5%. The expenditure incurred on these projects till April, 2013 is Rs. 24795.48 crore, which is 53.1% of the revised cost of the projects.

Figures are in Rs. Crore

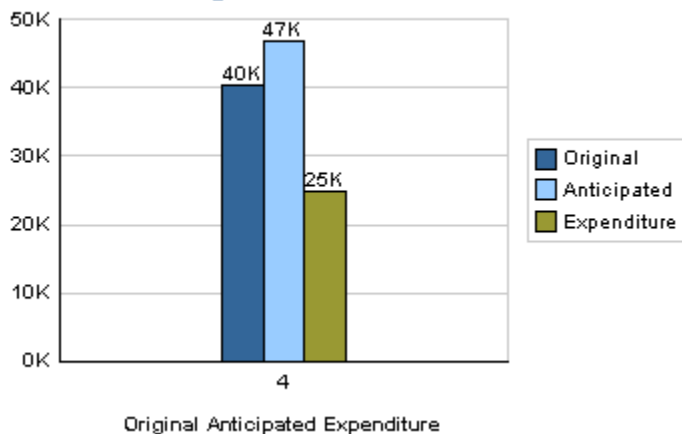

ANNEXURES

LIST OF CENTRAL SECTOR PROJECTS

SN	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	Andhra Pradesh	34	28405.55	36261.79	20104.54
2	Arunachal Pradesh	4	9512.22	14144.29	8767.52
3	Assam	34	22035.93	35386.06	23499.97
4	Bihar	30	26917.64	35131.24	24965.82
5	Chhatisgarh	24	58278.32	59362.92	19456.55
6	Delhi	4	38214.41	38194.82	3256.44
7	Goa	1	335.61	335.61	208.92
8	Gujarat	22	33405.07	33607.01	11472.92
9	Haryana	8	4054.38	5736.96	7034.86
10	Himachal Pradesh	5	13355.57	17246.69	13162.56
11	Jammu and Kashmir	10	14926.96	34825.56	14430.63
12	Jharkhand	23	14447.40	18650.84	9383.64
13	Karnataka	27	47076.40	56526.18	23094.72
14	Kerala	7	20376.67	21818.22	5558.14
15	Madhya pradesh	20	18545.58	18939.85	9486.67
16	Maharashtra	48	88574.45	100147.94	47555.21
17	Manipur	1	727.56	4453.50	1370.28
18	Meghalaya	2	762.00	762.00	463.70
19	Mizoram	2	1532.97	3297.97	461.93
20	Multi State	112	146738.66	157714.01	74846.57
21	Nagaland	1	850.00	2446.81	8.45
22	Odisha	30	56171.63	63436.93	37634.87
23	Punjab	6	3542.01	4483.78	3899.94
24	Rajasthan	14	21115.76	20927.99	8101.08
25	Sikkim	2	1648.94	3690.04	285.49
26	Tamil Nadu	32	48788.07	60101.42	40994.97
27	Tripura	3	1522.39	2018.85	1167.98
28	Uttar Pradesh	28	21622.60	25904.68	13350.71
29	Uttarakhand	5	7624.21	8564.64	2565.05
30	West Bengal	27	46938.87	59049.28	29686.92
TOTAL		566	798047.83	943167.88	456277.05

List of Projects Ahead of Schedule

							(Apr,2013)
						Date of Commissioning	
S.No	Project	Date of Approval	Original /Revised Cost (Rs. crore)	Anticipated (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Power</u>						
1	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID [N16000144]	9/2012	1,508.74 -	1,508.74	49.70	06/2016 -	04/2015
2	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID [N18000137]	9/2012	1,935.35 -	1,935.35	157.10	12/2014 -	11/2014
	Total		3,444.09 -	3,444.09	206.80		
	<u>Shipping & Ports</u>						
3	Acquisition of three(3) nos of 6500TEU Cellular container vessels from M/S stx shipbuilding co. ltd. - [N25000052]	10/2010	1,028.10 1,012.23	1,012.23	554.60	12/2013 11/2013	11/2013
	Total		1,028.10 -	1,012.23	554.60		
	Grand Total		4,472.19	4,456.32	761.40		

List of project Without Original Date of Commissioning

(Apr,2013)

Date of Commissioning									
S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumm. Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
<u>Petroleum</u>									
1	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 898.00	898.00	986.69	- -	08/2013	-	52/53
	Total		756.00 -	898.00	986.69				52/53
<u>Power</u>									
2	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 -	623.44	527.59	- -	07/2013	-	10/29
	Total		421.01 -	623.44	527.59				10/29
<u>Railways</u>									
3	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pradesh	09/1996	156.00 156.00	406.40	328.82	- -	06/2013	-	0/0
4	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	194.91	- -	12/2013	-	0/0
5	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 323.40	750.89	511.30	- -	03/2014	-	0/1
6	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Odisha	04/1994	355.38 470.21	1,995.25	243.58	- -	03/2014	-	0/0
7	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 915.70	2,232.50	1,787.92	- -	03/2014	-	0/0
8	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	230.03	145.76	- -	03/2014	-	0/0
9	New BG Rly line from Eklakhi-Balurghat including G - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	703.17	249.01	- -	03/2015	-	0/0
10	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 200.00	385.20	131.55	- -	03/2015	-	0/0
11	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	359.86	1.22	- -	03/2015	-	0/0
	Total		2,884.02 -	7,649.23	3,594.07				0/1
<u>Road Transport & Highways</u>									
12	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00 -	680.00	-	- -	04/2013	-	2/2
13	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI,Karnataka	09/2010	946.00 -	946.00	1,485.60	- -	06/2013	-	3/3

Date of Commissioning									
S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumm. Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
14	DEVIHALLI-HASSAN - [N24000152]NHAI, Karnataka	12/2010	453.00	453.00	524.25	-	06/2013	-	1/1
15	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI, Karnataka	12/2010	480.00	480.00	488.69	-	10/2013	-	2/2
16	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI, Karnataka	03/2011	839.00	839.00	570.06	-	12/2013	-	0/1
17	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI, Karnataka	09/2010	671.00	671.00	737.54	-	06/2014	-	2/3
	Total		4,069.00	4,069.00	3,806.14				10/12
			-						
Grand Total			8,130.03	13,239.67	8,914.49				72/95

List of project Without Date of Commissioning

Date of Commissioning					
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
<u>Atomic Energy</u>					
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00	12/2008	03/2013
			-	-	
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVINI,Tamil Nadu	09/2003	3,492.00	09/2010	-
			-	-	
	Total		16,663.00		
			-		
<u>Civil Aviation</u>					
3	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00	01/2011	02/2012
			2,015.00	02/2012	
4	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51	05/2011	03/2013
			-	-	
	Total		3,750.51		
			-		
<u>Coal</u>					
5	KUSMUNDA EXPN.OCP(SECL)(10-15)MTY - [N06000008]SECL,Chhatisgarh	06/2008	1,188.31	03/2013	03/2013
			-	-	
6	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	09/2007	467.78	03/2013	03/2013
			-	-	
7	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,Andhra Pradesh	11/2012	430.14	-	-
			-	-	
8	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03	03/2012	-
			-	-	
	Total		2,335.26		
			-		
<u>Fertilisers</u>					
9	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,Punjab	01/2010	1,478.63	01/2013	03/2013
			-	-	
	Total		1,478.63		
			-		
<u>Petroleum</u>					
10	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00	-	03/2013
			394.00	-	
11	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE - [N16000070]GAIL,Multi State	07/2009	238.68	01/2012	-
			-	-	
12	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18	01/2013	-
			-	-	
13	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,Multi State	08/2009	1,793.00	09/2012	-
			-	-	
14	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00	-	-
			-	-	
15	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32	03/2012	-
			-	-	

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
16	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL, Multi State	12/2009	540.92 -	07/2012 07/2012	-
17	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJEC - [N16000129]GAIL, Multi State	06/2009	2,915.00 -	12/2012 -	-
18	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]Mangalore Refin, Karnataka	07/2010	1,043.57 -	04/2012 -	-
	Total		16,398.67 -		
Power					
19	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC, Jammu and Kashmir	08/2006	621.26 -	02/2011 10/2012	01/2013
20	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL, Tamil Nadu	05/2005	1,779.29 2,159.07	09/2008 -	03/2013
21	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL, Maharashtra	12/2007	477.69 -	09/2010 -	03/2013
22	MOUDA STTP (NTPC) - [N18000048]NTPC, Maharashtra	11/2008	5,459.28 -	08/2012 -	03/2013
23	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC, Madhya Pradesh	01/2009	5,915.00 -	10/2012 -	03/2013
24	KAIGA 3 and 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL, Karnataka	03/2005	596.45 1,007.16	12/2007 12/2009	-
	Total		14,848.97 -		
Railways					
25	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER, Odisha	02/1996	57.94 604.04	03/1998 08/2005	08/2005
26	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR - [220100258]NR, Multi State	03/2002	409.00 625.30	06/2007 -	06/2007
27	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR, Andhra Pradesh	07/1998	125.00 363.26	07/2008 -	07/2008
28	GULBARGA-BIDAR, SCR(NL) - [220100254]SCR, Karnataka	02/1998	242.42 369.70	- 05/2009	05/2009
29	KODERMA GIRIDH (NL), ECR - [220100306]ECR, Jharkhand	04/1996	371.36 768.87	- 03/2010	03/2010
30	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP, West Bengal	03/2000	907.69 3,156.32	12/2006 08/2010	08/2010
31	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER, West Bengal	04/2004	225.68 293.74	12/2010 12/2010	12/2010
32	AMRAVATI-NARKHER NL(CR) - [220100118]CR, Maharashtra	06/1994	120.90 663.10	06/1999 03/2011	03/2011
33	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR, Multi State	12/2006	170.00 170.00	03/2011 03/2011	03/2011
34	BARDHAMAN-KATWA (GC) - [N22000091]ER, West Bengal	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011
35	CALICUT-MANGALORE (DL) (SR) - [220100151]SR, Multi State	02/1996	240.00 -	- -	02/2012
36	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, West Bengal	04/2000	157.96 1,188.91	- 12/2009	02/2012
37	Dakshin-barasal-lakshmikantapur - [N22000116]ER, West Bengal	04/2009	259.51 533.38	12/2011 02/2012	02/2012

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
38	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	- -	03/2012
39	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	02/2009 -	03/2012
40	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	- -	03/2012
41	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 381.17	- -	03/2012
42	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	- -	03/2012
43	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	- -	03/2012
44	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 155.00	- -	10/2012
45	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	- -	12/2012
46	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 194.07	06/2004 -	12/2012
47	JIND-SONEPAT (NL),NR - [220100280]NR,Haryana	01/2004	190.81 238.56	03/2012 03/2012	12/2012
48	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	- -	12/2012
49	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	- -	01/2013
50	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241]NR,Punjab	07/1998	248.44 576.27	12/2012 01/2013	02/2013
51	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	12/2012 12/2012	02/2013
52	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	- -	02/2013
53	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand	04/2008	167.73 167.73	03/2012 -	02/2013
54	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	03/1995 -	03/2013
55	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 900.05	12/2011 12/2011	03/2013
56	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	- -	03/2013
57	KADUR-CHIKMAGALUR-SAKLIESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	03/2012 03/2012	03/2013
58	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,577.45	- -	03/2013
59	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	- -	03/2013
60	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	02/2011 02/2011	03/2013
61	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	03/2012 03/2013	03/2013
62	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	03/2012 03/2013	03/2013
63	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.14 385.60	03/2013 -	03/2013
64	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	12/2012 -	-

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
65	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	03/1998 -	-
66	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	- -	-
67	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Odisha	04/1996	301.64 -	- 09/2009	-
68	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhand	04/2002	459.91 418.17	- -	-
69	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	-
70	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 380.00	03/2009 11/2012	-
71	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 -	02/2006 -	-
72	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-
73	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	03/2010 -	-
74	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,Uttar Pradesh	03/2013	307.00 -	- -	-
75	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,Multi State	03/2007	243.78 -	- -	-
76	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,Uttar Pradesh	03/2008	195.64 -	- -	-
77	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,Uttar Pradesh	03/2012	160.89 -	- -	-
78	CHHAPRA-BALLIA UP - [N22000134]NER,Multi State	03/2013	295.00 -	- -	-
79	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,Uttar Pradesh	03/2013	643.00 -	- -	-
80	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	- 03/2010	-
81	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 514.68	- -	-
82	NANGALDAM-TALWARA(NL),NR - [220100188]NR,Multi State	03/1981	37.68 450.00	07/2012 -	-
83	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1997	227.00 997.58	- -	-
84	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhand	03/1999	491.19 2,957.21	07/2005 -	-
85	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	05/2008 03/2011	-
86	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	03/2012 08/2012	-
87	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	- -	-
88	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 100.00	- -	-
89	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,047.00	- -	-
90	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 901.62	- -	-
91	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	- -	-

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
92	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar	04/2001	104.79 -	- -	-
93	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya Pradesh	04/2001	727.13 727.13	- -	-
94	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Odisha	04/2005	726.96 810.78	- -	-
95	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	- -	-
96	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	- -	-
97	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 125.00	- -	-
98	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 456.00	- -	-
99	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	- -	-
100	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya Pradesh	04/2008	603.04 603.04	03/2012 -	-
101	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24 -	03/2012 -	-
102	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	03/2011 -	-
	Total		22,743.32 -		
<u>Road Transport & Highways</u>					
103	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,Jammu and Kashmir	12/2003	166.27 -	03/2008 -	03/2013
104	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	07/2008 -	03/2013
	Total		391.27 -		
<u>Shipping & Ports</u>					
105	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 1,571.60	10/2008 -	10/2008
106	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Odisha	12/2005	154.84 -	- 01/2009	01/2009
107	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	04/2009 11/2009	02/2011
108	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	03/2012 -	03/2012
109	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	12/2011 10/2012	10/2012
110	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	06/2010 -	11/2012
111	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	02/2011 -	12/2012
112	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	03/2011 -	03/2013
113	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	10/2008 11/2010	-

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
	Total		6,210.04		
			-		
	<u>Telecommunications</u>				
114	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94	12/2008	12/2012
			-	-	
115	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhand	03/2008	328.13	03/2009	01/2013
			-	-	
116	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00	02/2007	02/2013
			-	03/2012	
117	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00	02/2007	-
			-	-	
118	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]MTNL,Maharashtra	06/2006	231.38	10/2007	-
			-	-	
119	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88	03/2010	-
			-	-	
120	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65	03/2010	-
			-	-	
121	DELHI CONVERGENT BILLING AND CRM PE-5834 - [N26000099]MTNL,Delhi	02/2006	229.41	03/2012	-
			-	-	
	Total		2,764.39		
			-		
	<u>Urban Development</u>				
122	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00	06/2011	03/2013
			-	-	
123	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18	04/2009	-
			173.08	-	
	Total		6,509.18		
			-		
	<u>Water Resources</u>				
124	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90	12/2007	12/2012
			-	-	
	Total		542.90		
			-		
	Grand Total		94,636.14		

List of Projects Without Milestones

(Apr,2013)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
<u>Civil Aviation</u>						
1	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	01/2011 02/2012	02/2012	0/0
2	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	05/2011 -	03/2013	0/0
3	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00 -	06/2013 -	06/2013	0/0
4	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61 -	05/2012 -	06/2013	0/0
5	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	01/2011 04/2013	12/2013	0/0
6	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MO - [N04000070]AAI,Punjab	02/2011	452.00 -	03/2015 -	03/2015	0/0
	Total		5,473.58 -			0/0
<u>Coal</u>						
7	Muraidih UG - [N06000096]BCCL,Jharkhand	02/2011	339.88 -	04/2014 -	04/2014	0/0
8	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhand	08/2011	1,230.27 -	04/2015 -	04/2015	0/0
	Total		1,570.15 -			0/0
<u>Steel</u>						
9	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, Chattisga - [N12000078]SAIL,Chhatisgarh	07/2012	332.65 -	08/2014 -	08/2014	0/0
10	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Oddisha - [N12000079]SAIL,Odisha	01/2012	254.90 -	12/2014 -	12/2014	0/0
	Total		587.55 -			0/0
<u>Petroleum</u>						
11	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]Mangalore Refin,Karnataka	07/2010	1,043.57 -	04/2012 -	01/2013	0/0
12	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,Multi State	02/2011	913.00 -	07/2015 -	07/2015	0/0
13	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	12/2008 04/2013	04/2013	0/0
14	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	09/2010 03/2012	04/2013	0/0
15	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	03/2013 -	04/2013	0/0
16	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	03/2010 03/2012	05/2013	0/0
17	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	05/2010 03/2013	05/2013	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
18	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	07/2010 05/2012	05/2013	0/0
19	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	03/2011 05/2011	05/2013	0/0
20	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	04/2006 06/2012	06/2013	0/0
21	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 -	06/2012 -	06/2013	0/0
22	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	08/2012 -	06/2013	0/0
23	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	08/2009	246.81 276.83	04/2012 -	06/2013	0/0
24	Capacity Augmentation of Kota Piyala Section of MMBPL Pipeli - [N16000153]BPCL,Rajasthan	04/2011	152.89 -	06/2013 -	06/2013	0/0
25	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	12/2011 -	07/2013	0/0
26	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	09/2012 -	09/2013	0/0
27	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	09/2012 -	09/2013	0/0
28	DBPL-II - [N16000147]GAIL,Multi State	06/2009	486.00 -	09/2013 -	09/2013	0/0
29	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	11/2012 -	10/2013	0/0
30	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	03/2013 -	11/2013	0/0
31	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79 -	05/2013 -	11/2013	0/0
32	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	08/2010 03/2012	12/2013	0/0
33	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	09/2011 -	12/2013	0/0
34	Wax Project - [N16000101]NRL,Assam	06/2010	576.60 -	12/2013 -	12/2013	0/0
35	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	01/2014 -	01/2014	0/0
36	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	08/2013 -	01/2014	0/0
37	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00 -	02/2014 -	02/2014	0/0
38	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	03/2013 -	03/2014	0/0
39	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	06/2012 -	03/2014	0/0
40	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 5,916.65	03/2013 03/2014	04/2014	0/0
41	IOR of B-173A Field - [N16000140]ONGC,Multi State	01/2012	352.49 -	03/2014 -	04/2014	0/0
42	Development of C-26 Cluster Fields - [N16000133]ONGC,Maharashtra	03/2012	2,592.17 -	05/2014 -	05/2014	0/0
43	Pipeline Replacement Project-3 - [N16000137]ONGC,Multi State	04/2012	2,547.26 -	05/2014 -	05/2014	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
44	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	10/2010 -	12/2014	0/0
45	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10 -	12/2014 -	12/2014	0/0
46	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63 -	12/2014 -	12/2014	0/0
47	Development of Western Periphery of MH South Field - [N16000136]ONGC,Multi State	04/2012	600.17 -	12/2014 -	12/2014	0/0
48	Replacement of CDU/VDU at Mumbai Refinery - [N16000142]BPCL,Maharashtra	01/1999	1,419.00 -	12/2014 -	12/2014	0/0
49	Mounded Bullet - [N16000154]CPCL,Tamil Nadu	12/2012	279.00 -	12/2014 -	12/2014	0/0
50	Integrated Development of B-127 fields - [N16000131]ONGC,Maharashtra	12/2011	2,059.63 -	03/2015 -	03/2015	0/0
51	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00 -	04/2015 -	04/2015	0/0
52	Heera and South Heera Redevelopment Ph-II - [N16000132]ONGC,Maharashtra	03/2012	5,608.40 -	05/2015 -	05/2015	0/0
53	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,Multi State	08/2011	586.00 -	07/2015 -	08/2015	0/0
54	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,Karnataka	11/2012	666.00 -	11/2015 -	11/2015	0/0
55	I REP - [N16000143]BPCL,Kerala	01/1999	14,225.00 -	12/2015 -	05/2016	0/0
56	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	01/2013 -	-	0/0
57	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	- -	-	0/0
	Total		102,015.78 -			0/0
Power						
58	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93 -	07/2013 -	07/2013	0/0
59	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	09/2009 06/2013	03/2014	0/0
60	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BA - [N18000124]PGCIL,Madhya pradesh	03/2012	213.78 -	03/2014 -	03/2014	0/0
61	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARK - [N18000113]PGCIL,Multi State	12/2011	2,422.66 -	08/2014 -	08/2014	0/0
62	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123]PGCIL,Multi State	03/2012	198.63 -	09/2014 -	09/2014	0/0
63	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]PGCIL,Multi State	12/2012	156.04 -	10/2014 -	10/2014	0/0
64	COMMON TRANSMISSION SCHEME WITH ISSG - [N18000139]PGCIL,Tamil Nadu	01/2013	182.80 -	10/2014 -	10/2014	0/0
65	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,Multi State	11/2011	723.63 -	11/2014 -	11/2014	0/0
66	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,Multi State	06/2012	1,263.26 -	11/2014 -	11/2014	0/0
67	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,Multi State	09/2012	1,935.35 -	12/2014 -	12/2014	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
68	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP P - [N18000120]PGCIL,Maharashtra	02/2012	1,310.85 -	02/2015 -	02/2015	0/0
69	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]PGCIL,Multi State	09/2012	803.34 -	03/2015 -	03/2015	0/0
70	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,Multi State	09/2012	524.40 -	04/2015 -	05/2015	0/0
71	COMMON TR. SYS. ASSOCIATED WITH EAST A.P - [N18000143]PGCIL,Multi State	03/2013	514.20 -	06/2015 -	06/2015	0/0
72	COMMON SYS. ASSOCIATED PART- B - [N18000144]PGCIL,Multi State	03/2013	2,514.88 -	12/2015 -	12/2015	0/0
73	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,Multi State	09/2012	1,508.74 -	06/2016 -	06/2016	0/0
74	Lata-Tapovan HPP 3x57MW - [N18000142]NTPC,Uttarakhand	07/2012	1,527.00 -	08/2017 -	08/2017	0/0
Total			17,042.87 -			0/0
<u>Railways</u>						
75	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Odisha	02/1996	57.94 604.04	03/1998 08/2005	08/2005	0/0
76	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,Multi State	03/2002	409.00 625.30	06/2007 -	06/2007	0/0
77	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	07/2008 -	07/2008	0/0
78	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	- 05/2009	05/2009	0/0
79	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36 768.87	- 03/2010	03/2010	0/0
80	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 3,156.32	12/2006 08/2010	08/2010	0/0
81	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 293.74	12/2010 12/2010	12/2010	0/0
82	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	06/1999 03/2011	03/2011	0/0
83	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	03/2011 03/2011	03/2011	0/0
84	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011	0/0
85	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	- -	02/2012	0/0
86	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	- 12/2009	02/2012	0/0
87	Dakshin-barasal-Iakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	12/2011 02/2012	02/2012	0/0
88	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	- -	03/2012	0/0
89	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	02/2009 -	03/2012	0/0
90	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	- -	03/2012	0/0
91	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 381.17	- -	03/2012	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
92	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	- -	03/2012	0/0
93	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	- -	03/2012	0/0
94	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 155.00	- -	10/2012	0/0
95	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	- -	12/2012	0/0
96	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 194.07	06/2004 -	12/2012	0/0
97	JIND-SONEPAT (NL),NR - [220100280]NR,Haryana	01/2004	190.81 238.56	03/2012 03/2012	12/2012	0/0
98	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	- -	12/2012	0/0
99	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	- -	01/2013	0/0
100	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241]NR,Punjab	07/1998	248.44 576.27	12/2012 01/2013	02/2013	0/0
101	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	12/2012 12/2012	02/2013	0/0
102	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	- -	02/2013	0/0
103	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand	04/2008	167.73 167.73	03/2012 -	02/2013	0/0
104	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	03/1995 -	03/2013	0/0
105	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 900.05	12/2011 12/2011	03/2013	0/0
106	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	- -	03/2013	0/0
107	KADUR-CHIKMAGALUR-SAKLSEHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	03/2012 03/2012	03/2013	0/0
108	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,577.45	- -	03/2013	0/0
109	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	02/2011 02/2011	03/2013	0/0
110	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	03/2012 03/2013	03/2013	0/0
111	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	03/2012 03/2013	03/2013	0/0
112	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.14 385.60	03/2013 -	03/2013	0/0
113	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Odisha	04/1993	100.00 142.98	03/2002 -	06/2013	0/0
114	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pradesh	09/1996	156.00 156.00	- -	06/2013	0/0
115	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,Multi State	04/1986	158.77 580.83	03/1994 -	10/2013	0/0
116	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 427.21	12/2009 03/2011	10/2013	0/0
117	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	12/2011 11/2013	11/2013	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
118	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	- -	12/2013	0/0
119	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 224.89	03/2012 -	12/2013	0/0
120	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 207.52	12/2012 -	12/2013	0/0
121	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	03/2004 12/2010	03/2014	0/0
122	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Odisha	04/1994	355.38 470.21	- -	03/2014	0/0
123	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 915.70	- -	03/2014	0/0
124	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	- -	03/2014	0/0
125	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	06/2013 06/2013	03/2014	0/0
126	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	03/2013 -	03/2014	0/0
127	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 653.19	03/2014 -	03/2014	0/0
128	Suratpura - Hanumangarh - Sriganaganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 516.23	03/2014 -	03/2014	0/0
129	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	03/2014 -	03/2014	0/0
130	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 -	02/2006 -	06/2014	0/0
131	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Odisha	04/1999	166.16 -	02/2009 02/2009	08/2014	0/0
132	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Odisha	04/2000	133.41 207.00	03/2009 03/2009	08/2014	0/0
133	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,Uttar Pradesh	09/2001	129.70 245.39	12/2008 -	09/2014	0/0
134	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 2,363.00	03/2009 12/2012	12/2014	0/0
135	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Odisha	04/1998	183.23 -	02/2015 -	02/2015	0/0
136	New BG Rly line from Eklakhi-Balurghat including G - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	- -	03/2015	0/0
137	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	03/2007 03/2007	03/2015	0/0
138	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	12/2010 12/2010	03/2015	0/0
139	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 733.00	12/2008 -	03/2015	0/0
140	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 200.00	- -	03/2015	0/0
141	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	- -	03/2015	0/0
142	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 829.74	03/2015 -	03/2015	0/0
143	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	12/2012 -	03/2015	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
144	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	03/2009 -	03/2015	0/0
145	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	04/2008 03/2014	12/2015	0/0
146	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 2,921.00	10/2007 12/2012	12/2015	0/0
147	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 529.23	02/2010 11/2012	12/2015	0/0
148	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	03/2010 -	12/2015	0/0
149	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 813.34	03/2014 -	12/2015	0/0
150	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	03/2014 03/2016	03/2016	0/0
151	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	03/2014 -	03/2016	0/0
152	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	03/2016 -	03/2016	0/0
153	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 -	03/2016 -	03/2016	0/0
154	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	06/2005 07/2011	06/2016	0/0
155	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	03/2016 -	06/2016	0/0
156	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,028.05	03/2005 12/2008	12/2016	0/0
157	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	03/2011 03/2014	03/2017	0/0
158	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,Uttar Pradesh	04/2006	325.00 325.00	03/2010 03/2017	03/2017	0/0
159	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	04/2014 -	03/2017	0/0
160	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	12/2015 -	03/2017	0/0
161	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 850.00	03/2015 -	03/2017	0/0
162	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,Jammu and Kashmir	03/1995	2,500.00 2,500.00	03/2001 -	12/2017	0/0
163	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	12/2012 -	-	0/0
164	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	03/1998 -	-	0/0
165	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	- -	-	0/0
166	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	04/2003 03/2010	-	0/0
167	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Odisha	04/1996	301.64 -	- 09/2009	-	0/0
168	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhand	04/2002	459.91 418.17	- -	-	0/0
169	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	- 03/2009	-	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
170	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	-	0/0
171	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 380.00	03/2009 11/2012	-	0/0
172	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-	0/0
173	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	03/2010 -	-	0/0
174	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	- 03/2010	-	0/0
175	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 1,010.00	- -	-	0/0
176	NANGALDAM-TALWARA(NL),NR - [220100188]NR,Multi State	03/1981	37.68 450.00	07/2012 -	-	0/0
177	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1997	227.00 997.58	- -	-	0/0
178	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhand	03/1999	491.19 2,957.21	07/2005 -	-	0/0
179	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	05/2008 03/2011	-	0/0
180	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	03/2012 08/2012	-	0/0
181	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	- -	-	0/0
182	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 100.00	- -	-	0/0
183	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,047.00	- -	-	0/0
184	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 901.62	- -	-	0/0
185	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	- -	-	0/0
186	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar	04/2001	104.79 -	- -	-	0/0
187	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	- -	-	0/0
188	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Odisha	04/2005	726.96 810.78	- -	-	0/0
189	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	- -	-	0/0
190	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	- -	-	0/0
191	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 125.00	- -	-	0/0
192	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 456.00	- -	-	0/0
193	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	- -	-	0/0
194	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 603.04	03/2012 -	-	0/0
195	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24 -	03/2012 -	-	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
196	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	03/2011 -	-	0/0
	Total		59,987.39 -			0/0
Road Transport & Highways						
197	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00 -	09/2008 -	03/2013	0/0
198	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,Jammu and Kashmir	12/2003	166.27 -	03/2008 -	03/2013	0/0
199	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	07/2008 -	03/2013	0/0
200	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Odisha	04/2000	225.00 -	04/2004 -	04/2013	0/0
201	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68 -	03/2008 -	04/2013	0/0
202	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	06/2009 -	04/2013	0/0
203	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Odisha	04/2000	263.27 -	02/2004 -	04/2013	0/0
204	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93 -	10/2009 -	04/2013	0/0
205	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Odisha	04/2000	228.70 -	02/2004 -	04/2013	0/0
206	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06 -	12/2012 -	04/2013	0/0
207	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh	10/2010	1,175.00 -	04/2013 -	04/2013	0/0
208	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56 -	02/2012 -	04/2013	0/0
209	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94 -	09/2008 -	05/2013	0/0
210	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	06/2008 -	05/2013	0/0
211	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	06/2008 -	05/2013	0/0
212	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00 -	01/2011 -	05/2013	0/0
213	Trichy Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00 -	05/2013 -	05/2013	0/0
214	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	08/2004 07/2010	06/2013	0/0
215	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	08/2004 -	06/2013	0/0
216	RAJMARG CHORAH TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	10/2008 -	06/2013	0/0
217	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00 -	03/2008 -	06/2013	0/0
218	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00 -	12/2008 -	06/2013	0/0
219	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06 -	09/2009 -	06/2013	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
220	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00 -	05/2010 -	06/2013	0/0
221	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00 -	07/2012 -	06/2013	0/0
222	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00 -	05/2012 -	06/2013	0/0
223	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75 -	08/2011 -	06/2013	0/0
224	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30 -	10/2011 -	06/2013	0/0
225	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhand	08/2010	625.07 -	01/2013 -	06/2013	0/0
226	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00 -	11/2012 -	06/2013	0/0
227	MURADABAD-BAREILY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00 -	06/2013 -	06/2013	0/0
228	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50 -	06/2013 -	06/2013	0/0
229	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu	06/2011	600.00 -	06/2013 -	06/2013	0/0
230	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00 -	12/2009 -	07/2013	0/0
231	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00 -	03/2013 -	07/2013	0/0
232	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	593.00 -	07/2013 -	07/2013	0/0
233	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,Bihar	01/2011	575.00 -	07/2013 -	07/2013	0/0
234	JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan	08/2010	267.81 -	02/2013 -	07/2013	0/0
235	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00 -	11/2011 -	08/2013	0/0
236	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat	03/2011	785.50 -	08/2013 -	08/2013	0/0
237	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00 -	08/2013 -	08/2013	0/0
238	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00 -	08/2013 -	08/2013	0/0
239	BHUBANESWAR TO PURI - [N24000195]NHAI,Odisha	03/2011	500.29 -	08/2013 -	08/2013	0/0
240	4-laning of Faraka-Raiganj - [N24000202]NHAI,Multi State	02/2011	1,078.84 -	08/2013 -	08/2013	0/0
241	4-laning of Brahampore-Faraka - [N24000203]NHAI,Multi State	02/2011	998.79 -	08/2013 -	08/2013	0/0
242	4-laning of Raiganj-Dalkola - [N24000204]NHAI,Multi State	02/2011	580.43 -	08/2013 -	08/2013	0/0
243	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	05/2008 -	09/2013	0/0
244	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	10/2008 -	09/2013	0/0
245	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00 -	06/2008 -	09/2013	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
246	NALBARI TO BIJINI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00	06/2008	09/2013	0/0
247	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00	07/2010	09/2013	0/0
248	New 4 Lane elevated road from chennai airport - [N24000139]NHAI,Tamil Nadu	09/2010	1,655.00	09/2013	09/2013	0/0
249	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00	05/2013	09/2013	0/0
250	BAREILY-SITAPUR - [N24000200]NHAI,Uttar Pradesh	03/2011	1,046.00	09/2013	09/2013	0/0
251	Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00	05/2012	10/2013	0/0
252	PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar	08/2010	671.30	02/2013	10/2013	0/0
253	Tirupati - Chennai - [N24000178]NHAI,Tamil Nadu	04/2011	571.00	10/2013	10/2013	0/0
254	BHOPAL-SANCHI - [N24000192]NHAI, Madhya pradesh	10/2011	209.00	01/2013	10/2013	0/0
255	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00	09/2007	11/2013	0/0
256	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00	11/2013	11/2013	0/0
257	ROHTAK-BAWAL - [N24000169]NHAI,Haryana	05/2011	650.00	11/2013	11/2013	0/0
258	Muzafarpur - Sonbarsa - [N24000174]NHAI,Bihar	05/2011	511.54	11/2013	11/2013	0/0
259	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI,Bihar	05/2011	511.54	11/2013	11/2013	0/0
260	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47	09/2007	12/2013	0/0
261	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00	10/2008	12/2013	0/0
262	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00	01/2009	12/2013	0/0
263	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00	05/2008	12/2013	0/0
264	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI, Madhya pradesh	12/2003	407.60	06/2010	12/2013	0/0
265	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52	06/2011	12/2013	0/0
266	Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10	09/2012	12/2013	0/0
267	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70	10/2011	12/2013	0/0
268	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI,Tamil Nadu	06/2011	535.00	12/2013	12/2013	0/0
269	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM. - [N24000172]NHAI,Tamil Nadu	09/2011	1,250.00	12/2013	12/2013	0/0
270	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI,Gujarat	09/2010	805.39	03/2013	12/2013	0/0
271	SAMAIKHIALI GANDHIDHAM - [N24000223]NHAI,Gujarat	09/2010	805.39	12/2013	12/2013	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
272	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI, Multi State	12/2003	232.45 -	09/2010 -	01/2014	0/0
273	JORBAT - BARAPANI - [N24000180]NHAI, Meghalaya	01/2011	536.00 -	01/2014 -	01/2014	0/0
274	PUNE-SHOLAPUR, Pkg-II - [N24000193]NHAI, Maharashtra	09/2011	835.00 -	01/2014 -	01/2014	0/0
275	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI, Odisha	07/2011	586.00 -	01/2014 -	01/2014	0/0
276	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, Uttar Pradesh	07/2012	291.36 -	01/2014 -	01/2014	0/0
277	INDORE-DEWAS(NH-3) - [N24000159]NHAI, Madhya Pradesh	11/2010	325.00 -	05/2013 -	02/2014	0/0
278	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI, Meghalaya	02/2011	226.00 -	02/2014 -	02/2014	0/0
279	4-laning of Barhi-Hazaribagh - [N24000191]NHAI, Jharkhand	02/2012	398.00 -	02/2014 -	02/2014	0/0
280	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI, Assam	12/2003	230.00 -	06/2005 -	03/2014	0/0
281	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI, Assam	12/2003	195.00 -	06/2008 -	03/2014	0/0
282	BIJNI TO ASSAM/WB BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI, Assam	12/2003	237.80 -	06/2008 -	03/2014	0/0
283	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, Assam	12/2003	175.96 -	04/2008 -	03/2014	0/0
284	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, Assam	12/2003	198.16 -	04/2008 -	03/2014	0/0
285	AGRA-BYPASS(NS-1/UP-1), KM 176.8-13.03 NH-2,3 - [N24000098]NHAI, Uttar Pradesh	12/2003	348.16 -	09/2007 -	03/2014	0/0
286	Chennai-Tada(Six lane) - [N24000129]NHAI, Tamil Nadu	04/2009	353.37 -	10/2011 -	03/2014	0/0
287	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI, Maharashtra	02/2011	193.45 -	11/2012 -	03/2014	0/0
288	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, Bihar	05/2011	351.54 -	05/2013 -	03/2014	0/0
289	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI, Multi State	09/2011	2,848.00 -	03/2014 -	03/2014	0/0
290	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, Bihar	09/2011	574.00 -	03/2014 -	03/2014	0/0
291	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, Multi State	09/2011	754.00 -	03/2013 -	03/2014	0/0
292	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI, Uttarakhand	11/2011	478.00 -	10/2013 -	03/2014	0/0
293	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI, Kerala	04/2011	682.00 -	10/2013 -	03/2014	0/0
294	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI, Assam	12/2003	212.00 -	09/2007 -	04/2014	0/0
295	PUNE-SATARA(NH-4) - [N24000156]NHAI, Maharashtra	10/2010	1,724.55 -	03/2013 -	04/2014	0/0
296	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, Bihar	05/2011	664.00 -	02/2014 -	04/2014	0/0
297	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, Bihar	10/2011	375.09 -	04/2014 -	04/2014	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
298	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHHTH 170 KM) - [N24000213]NHAI,Multi State	04/2012	624.00 -	04/2014 -	04/2014	0/0
299	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	02/2009 03/2014	05/2014	0/0
300	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00 -	04/2008 -	05/2014	0/0
301	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	07/2009 -	05/2014	0/0
302	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI,Andhra Pradesh	11/2011	1,535.00 -	05/2014 -	05/2014	0/0
303	2laning with PS Gopalganj-Chappra - [N24000190]NHAI,Bihar	12/2011	325.00 -	05/2014 -	05/2014	0/0
304	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,Odisha	11/2011	909.00 -	05/2014 -	05/2014	0/0
305	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00 -	10/2008 -	06/2014	0/0
306	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04 -	11/2008 -	06/2014	0/0
307	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,Jammu and Kashmir	07/2010	1,813.76 -	07/2013 -	06/2014	0/0
308	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88 -	07/2013 -	06/2014	0/0
309	SNG toBANL - [N24000189]NHAI,Jammu and Kashmir	06/2011	1,100.70 -	06/2014 -	06/2014	0/0
310	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,Rajasthan	12/2011	2,388.00 -	06/2014 -	06/2014	0/0
311	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]NHAI,Multi State	12/2011	1,047.00 -	06/2014 -	06/2014	0/0
312	PANVEL-INDAPUR - [N24000216]NHAI,Multi State	12/2011	942.69 -	06/2014 -	06/2014	0/0
313	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	02/2010 -	07/2014	0/0
314	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00 -	09/2013 -	07/2014	0/0
315	LUCKNOW-RAIBAREILI - [N24000207]NHAI,Uttar Pradesh	07/1999	635.90 -	07/2012 -	07/2014	0/0
316	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,West Bengal	02/2012	702.16 -	07/2014 -	07/2014	0/0
317	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,Bihar	07/2012	356.40 -	07/2014 -	07/2014	0/0
318	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,Uttar Pradesh	01/2013	373.47 -	07/2014 -	07/2014	0/0
319	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	09/2009 -	09/2014	0/0
320	PANIKHOLI-RIMOLI - [N24000197]NHAI,Odisha	03/2012	1,410.00 -	09/2014 -	09/2014	0/0
321	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,West Bengal	04/2012	1,396.18 -	09/2014 -	09/2014	0/0
322	PANIPAT-ROHTAK - [N24000151]NHAI,Haryana	04/2011	807.00 -	10/2014 -	10/2014	0/0
323	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,Maharashtra	04/2012	484.19 -	10/2014 -	10/2014	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
324	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,Uttar Pradesh	10/2012	250.50 -	10/2014 -	10/2014	0/0
325	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	04/2010 -	11/2014	0/0
326	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81 -	04/2009 -	12/2014	0/0
327	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	11/2008 -	12/2014	0/0
328	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	04/2009 -	12/2014	0/0
329	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00 -	02/2010 -	12/2014	0/0
330	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00 -	08/2012 -	03/2015	0/0
331	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,Multi State	10/2012	1,928.22 -	04/2015 -	04/2015	0/0
332	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,Multi State	12/2012	1,479.00 -	06/2015 -	06/2015	0/0
333	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	08/2014 -	07/2015	0/0
334	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,Multi State	02/2013	1,232.00 -	08/2015 -	08/2015	0/0
335	ETAWAH CHAKERI - [N24000219]NHAI,Uttar Pradesh	03/2013	1,573.00 -	09/2015 -	09/2015	0/0
336	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,Gujarat	01/2013	2,125.24 -	12/2015 -	12/2015	0/0
337	NASHRI CHANANI - [N24000162]NHAI,Jammu and Kashmir	06/2010	2,159.00 -	06/2015 -	05/2016	0/0
338	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,Jammu and Kashmir	07/2010	1,987.00 -	07/2015 -	06/2016	0/0
	Total		97,264.26 -			0/0
Shipping & Ports						
339	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 1,571.60	10/2008 -	10/2008	0/0
340	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	04/2009 11/2009	02/2011	0/0
341	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	03/2012 -	03/2012	0/0
342	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	12/2011 10/2012	10/2012	0/0
343	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	04/2011 -	11/2012	0/0
344	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	06/2010 -	11/2012	0/0
345	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	02/2011 -	12/2012	0/0
346	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	03/2011 -	03/2013	0/0
347	Setting up of Single Point Mooring (SPM) and allie - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -	05/2013 -	03/2013	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
348	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	01/2012 09/2012	04/2013	0/0
349	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 309.00	03/2006 06/2013	06/2013	0/0
350	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,Multi State	07/2011	220.49 -	01/2013 -	06/2013	0/0
351	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 532.83	12/2012 10/2013	10/2013	0/0
352	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	12/2013 10/2013	10/2013	0/0
353	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	02/2014 -	02/2014	0/0
354	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPL - [N25000062]SHIPP.,Multi State	01/2012	511.87 -	03/2014 -	03/2014	0/0
355	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	12/2010 09/2012	04/2014	0/0
356	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	10/2008 11/2010	-	0/0
	Total		15,462.28 -			0/0
Telecommunications						
357	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	12/2008 -	12/2012	0/0
358	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhand	03/2008	328.13 -	03/2009 -	01/2013	0/0
359	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 -	02/2007 03/2012	02/2013	0/0
360	DELHI CONVERGENT BILLING AND CRM PE-5834 - [N26000099]MTNL,Delhi	02/2006	229.41 -	03/2012 -	02/2013	0/0
361	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttarakhand	01/2009	149.15 -	06/2009 -	06/2013	0/0
362	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	01/2009 -	06/2013	0/0
363	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 -	11/2010 -	06/2013	0/0
364	Supply Installation testing and commissioning of Rural Wimax - [N26000100]BSNL,Multi State	07/2010	1,148.19 -	05/2011 -	06/2013	0/0
365	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	10/2010 -	09/2013	0/0
366	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	02/2007 12/2010	-	0/0
367	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]MTNL,Maharashtra	06/2006	231.38 -	10/2007 -	-	0/0
368	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	03/2010 -	-	0/0
369	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	03/2010 -	-	0/0
	Total		5,699.24 -			0/0

Urban Development

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
370	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00	09/2014	09/2014	0/0
			-	-		
371	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00	03/2016	03/2016	0/0
			-	-		
372	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18	04/2009	-	0/0
			173.08	-		
	Total		37,850.18			0/0
			-			
<u>Water Resources</u>						
373	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90	12/2007	12/2012	0/0
			-	-		
	Total		542.90			0/0
			-			
Grand Total			343,496.18			0/0

LIST OF ONSCHEDULE PROJECTS W.R.T. ORIGINAL

SN	PROJECT	SECTOR	DOA	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED
1	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II	Civil Aviation	02/2011	03/2015	03/2015	452.00	452.00
2	GAGAN PROJECT	Civil Aviation	09/2008	06/2013	06/2013	626.00	626.00
3	Moonidih XV Seam UG	Coal	08/2011	04/2015	04/2015	1230.27	1230.27
4	Muraidih UG Turn-key Project	Coal	02/2011	04/2014	04/2014	339.88	339.88
5	KARMA OCP (1.0MTY)	Coal	06/2009	03/2014	03/2014	162.46	162.46
6	Rajrappa RCE OCP (3.0 MTY)	Coal	12/2009	03/2016	03/2016	510.85	510.85
7	BHUBANESWARI OCP, MCL (20.0 Mty)	Coal	12/2007	03/2017	03/2017	490.00	490.10
8	GOPAL PRASAD OCP (15MTY)	Coal	02/2008	03/2015	03/2015	395.87	395.87
9	TALABIRA OCP	Coal	03/2008	03/2016	03/2016	447.72	447.72
10	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL)	Coal	06/2011	03/2018	03/2018	1131.28	1131.28
11	BLOCK-B OCP NCL (3.5 MTY)	Coal	06/2011	03/2015	03/2015	746.04	535.10
12	AMLOHRI EPR (NCL) (6 MTY , INCR.)	Coal	12/2009	03/2016	03/2016	1352.04	1143.54
13	BINA EXTN. PROJ(6.0 Mtpa)	Coal	11/2006	03/2014	03/2014	168.97	168.97
14	JALAGAM VENGALA RAO OCP-II	Coal	07/2011	03/2015	03/2015	447.06	447.06
15	Kistaram OCP	Coal	11/2010	03/2015	03/2015	242.29	242.29
16	RCE OF INDARAM OCP(1.20 MTPA)	Coal	07/2011	03/2015	03/2015	162.76	162.76
17	RKP OCP PHASE-I	Coal	03/2010	03/2015	03/2015	209.78	209.78
18	BAROUD OC EXPANSION (RCE)- 3MTY	Coal	04/2012	03/2016	03/2016	258.56	258.56
19	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	Coal	11/2009	03/2016	03/2016	150.59	198.59
20	Batura OCP (2.0 MTY)	Coal	09/2008	03/2015	03/2015	203.82	203.82
21	PELMA OCP(10.00MTY)	Coal	07/2008	03/2015	03/2015	448.32	448.32
22	Replacement of CDU/VDU at Mumbai Refinery	Petroleum	01/1999	12/2014	12/2014	1419.00	1419.00
23	Capacity Augmentation of Kota Piyala Section of MMBPL Pipeline	Petroleum	04/2011	06/2013	06/2013	152.89	152.89
24	Mounded Bullet Project at CPCL	Petroleum	12/2012	12/2014	12/2014	279.00	279.00
25	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA	Petroleum	08/2010	02/2014	02/2014	8140.00	8140.00
26	DABHOL BANGALORE PIPELINE PROJECT PHASE-II	Petroleum	06/2009	09/2013	09/2013	486.00	486.00
27	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	Petroleum	11/2012	11/2015	11/2015	666.00	666.00
28	REWARI KANPUR PIPELINE PROJECT	Petroleum	02/2012	11/2015	11/2015	1210.64	1210.64
29	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	Petroleum	11/2012	08/2014	08/2014	309.81	309.81
30	BUTENE-1 PROJECT AT PANIPAT	Petroleum	02/2012	03/2014	03/2014	190.00	190.00
31	PARADIP HALDIA DURGAPUR LPG PIPELINE	Petroleum	02/2011	07/2015	07/2015	913.00	913.00
32	Wax Project	Petroleum	06/2010	12/2013	12/2013	576.60	576.60

SN	PROJECT	SECTOR	DOA	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED
33	Pipeline Replacement Project-3	Petroleum	04/2012	05/2014	05/2014	2547.26	1417.00
34	Development of WO-16 Cluster Fields	Petroleum	06/2010	01/2014	01/2014	2523.00	2523.00
35	Ankleswar Redevelopment	Petroleum	11/2010	12/2014	12/2014	2189.63	2189.63
36	Heera and South Heera Redevelopment Ph-II	Petroleum	03/2012	05/2015	05/2015	5608.40	5608.40
37	Mehesana Redevelopment	Petroleum	11/2010	04/2015	04/2015	3823.00	3823.00
38	Ahmedabad Redevelopment	Petroleum	11/2010	12/2014	12/2014	1916.10	1916.10
39	Development of C-26 Cluster Fields	Petroleum	03/2012	05/2014	05/2014	2592.17	2592.17
40	Development of Western Periphery of MH South Field	Petroleum	04/2012	12/2014	12/2014	600.17	600.17
41	Integrated Development of B-127 fields	Petroleum	12/2011	03/2015	03/2015	2059.63	2665.65
42	SOLAPUR STPP	Power	03/2012	11/2016	11/2016	9395.18	9395.18
43	VINDHYACHAL STPP STAGE-V	Power	12/2011	08/2015	08/2015	3180.40	3180.40
44	KUDGI STPP STAGE 1	Power	12/2011	12/2016	12/2016	15166.19	15166.19
45	MOUDA STPP STAGE 2	Power	03/2012	09/2016	09/2016	7921.47	7921.47
46	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 x 800 MW)	Power	11/2012	05/2017	05/2017	11846.00	11846.00
47	Lata-Tapovan Hydro Electric Power Project 3x57 MW	Power	07/2012	08/2017	08/2017	1527.00	1527.00
48	SYSTEM STRENGTHENING XIII OF SR GRID	Power	10/2011	06/2014	06/2014	487.49	487.49
49	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B	Power	03/2013	12/2015	12/2015	2514.88	2514.88
50	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B	Power	02/2012	10/2014	10/2014	1927.16	1927.16
51	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID	Power	06/2012	11/2014	11/2014	1263.26	1263.26
52	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI	Power	09/2012	03/2015	03/2015	803.34	803.34
53	Transmission system for phase-I gen.proj.in orissa part-C	Power	03/2011	03/2014	03/2014	2569.25	2569.25
54	Establishment of pooling stations at Rajgarh and raipur for IPP generation projects in chattisgarh	Power	12/2010	08/2013	08/2013	1719.52	1719.52
55	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2	Power	12/2011	08/2014	08/2014	2422.66	2422.66
56	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED	Power	12/2011	02/2014	02/2014	552.44	552.44
57	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	Power	12/2011	08/2014	08/2014	1746.65	1746.65

SN	PROJECT	SECTOR	DOA	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED
58	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1	Power	03/2012	06/2014	06/2014	206.44	206.44
59	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED	Power	08/2011	10/2013	10/2013	425.51	425.51
60	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNAM OF ANDHRA PRADESH(PGCIL)	Power	08/2011	08/2014	08/2014	1637.34	1637.34
61	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD	Power	01/2012	01/2014	01/2014	259.28	259.28
62	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV	Power	11/2011	11/2014	11/2014	723.63	723.63
63	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH	Power	02/2012	02/2015	02/2015	1310.85	1310.85
64	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH	Power	03/2012	06/2015	06/2015	9569.76	9569.76
65	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH	Power	05/2011	05/2014	05/2014	1961.87	1961.87
66	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV	Power	12/2011	08/2014	08/2014	297.33	297.33
67	TRANSMISSION SYS ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1	Power	02/2012	08/2014	08/2014	324.33	324.33
68	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION	Power	03/2012	09/2014	09/2014	198.63	198.63
69	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A	Power	12/2012	10/2014	10/2014	156.04	156.04
70	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUB STATION AT KALA IN UT DNH	Power	07/2011	07/2013	07/2013	181.93	181.93
71	Common System Associated with Coastal Energen Private Limited and Ind-Barath Power(Madras) Limited L	Power	09/2011	09/2014	09/2014	1940.13	1940.13
72	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH	Power	09/2011	12/2013	12/2013	1366.34	1366.34
73	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH	Power	01/2012	01/2015	01/2015	1422.85	1422.85

SN	PROJECT	SECTOR	DOA	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED
74	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION)	Power	03/2012	03/2014	03/2014	213.78	213.78
75	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B	Power	02/2012	10/2014	10/2014	3201.44	3201.44
76	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1	Power	01/2013	10/2014	10/2014	182.80	182.80
77	COMMON TR. SYS. ASSOCIATED WITH EAST COAST & NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C	Power	03/2013	06/2015	06/2015	514.20	514.20
78	Transm System for development of Pooling strn. in NR part of West Bengal & Transfer of power from BHU	Power	04/2010	01/2015	01/2015	4404.57	4404.57
79	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN	Power	08/2011	12/2013	12/2013	1391.97	1391.97
80	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS	Power	12/2011	08/2014	08/2014	901.77	901.77
81	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPs GENERATION PROJECTS IN CHATTISGARH	Power	11/2011	07/2014	07/2014	2127.51	2127.51
82	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	Railways	03/2013	03/2016	03/2016	4874.58	4874.58
83	Suratpura - Hanumangarh - Sriganganagar Guage Conversion (NWR)	Railways	04/2008	03/2014	03/2014	516.23	516.23
84	Himmatnagar - Udaipur Gauge Canvession (NWR)	Railways	04/2008	03/2015	03/2015	829.74	829.74
85	Jaipur - Ringus - Churu and Sikar - Loharu Guage Conversion (NWR)	Railways	04/2008	03/2014	03/2014	653.19	653.46
86	New Work for Construction of Metro railway from NSCB Airport to New Garia VIA Rajarhat (MTP)	Railways	04/2010	03/2016	03/2016	3951.98	3951.98
87	New Work for Construction of Metro railway from Baranagar to Barrackpore and Dakshineshwar (MTP)	Railways	04/2010	03/2014	03/2014	2069.60	2069.60
88	New Work for Construction of Metro railway from Joka to Binoy Badal Dinesh Bagh.	Railways	04/2010	03/2016	03/2016	2619.02	2619.02
89	SUKINDA ROAD - ANGUL (NL)(ECOR)	Railways	04/1998	02/2015	02/2015	183.23	818.29
90	Udhna-Jalgaon with electrification(doubling) (WR)	Railways	04/2008	03/2014	03/2014	1389.62	1389.62
91	KRISHNANAGAR-BERHAMPUR	Road Transport & Highways	02/2012	07/2014	07/2014	702.16	702.16
92	PANVEL-INDAPUR	Road Transport & Highways	12/2011	06/2014	06/2014	942.69	942.69

SN	PROJECT	SECTOR	DOA	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED
93	ETAWAH CHAKERI	Road Transport & Highways	03/2013	09/2015	09/2015	1573.00	1573.00
94	4 LANNING OF AHMEDABAD TO GODHARA	Road Transport & Highways	12/2010	06/2013	06/2013	1008.50	1008.50
95	4 LANNING OF GODHARA TO GUJARAT/MP BORDER	Road Transport & Highways	03/2011	08/2013	08/2013	785.50	785.50
96	4-laning of Barhi-Hazaribagh	Road Transport & Highways	02/2012	02/2014	02/2014	398.00	398.00
97	BEAWAR-PALI-PINDWARA	Road Transport & Highways	12/2011	06/2014	06/2014	2388.00	2388.00
98	six laning of Chandikhol-Jagatpur-Bhubaneswar	Road Transport & Highways	12/2011	06/2014	06/2014	1047.00	1047.00
99	2 LANING WITH PS AGRA ALIGARH	Road Transport & Highways	10/2012	10/2014	10/2014	250.50	250.50
100	PANIPAT-ROHTAK	Road Transport & Highways	04/2011	10/2014	10/2014	807.00	807.00
101	New 4 Lane elevated road from chennai airport-maduravoyal NH no.4	Road Transport & Highways	09/2010	09/2013	09/2013	1655.00	1655.00
102	NAGPUR-WAINGANGA BRIDGE	Road Transport & Highways	04/2012	10/2014	10/2014	484.19	484.19
103	RANCHI-RARGA-JAMSETHPUR	Road Transport & Highways	12/2012	06/2015	06/2015	1479.00	1479.00
104	PANIKHOLI-RIMOLI	Road Transport & Highways	03/2012	09/2014	09/2014	1410.00	1410.00
105	DELHI AGRA APPROVED LENGTH 180.0 KM	Road Transport & Highways	10/2012	04/2015	04/2015	1928.22	1928.22
106	DEOLI-KOTA	Road Transport & Highways	01/2011	07/2013	07/2013	593.00	593.00
107	MURADABAD-BAREILY	Road Transport & Highways	04/2010	06/2013	06/2013	1267.00	1267.00
108	Indore-Jhabua-Gujrat/MP	Road Transport & Highways	10/2010	04/2013	04/2013	1175.00	1175.00
109	ROHTAK-BAWAL	Road Transport & Highways	05/2011	11/2013	11/2013	650.00	650.00
110	2-LANNING OF SHILONG BYPASS	Road Transport & Highways	02/2011	02/2014	02/2014	226.00	226.00
111	2laning with PS Gopalganj-Chappra	Road Transport & Highways	12/2011	05/2014	05/2014	325.00	325.00

SN	PROJECT	SECTOR	DOA	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED
112	PUNE-SHOLAPUR,Pkg-II	Road Transport & Highways	09/2011	01/2014	01/2014	835.00	835.00
113	BAREILY-SITAPUR	Road Transport & Highways	03/2011	09/2013	09/2013	1046.00	1046.00
114	4-laning of Brahampore-Faraka	Road Transport & Highways	02/2011	08/2013	08/2013	998.79	998.79
115	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI	Road Transport & Highways	07/2012	07/2014	07/2014	356.40	356.40
116	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM)	Road Transport & Highways	04/2012	04/2014	04/2014	624.00	624.00
117	SAMAIKHALI GANDHIDHAM	Road Transport & Highways	09/2010	12/2013	12/2013	805.39	805.39
118	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00	Road Transport & Highways	06/2011	12/2013	12/2013	535.00	535.00
119	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	Road Transport & Highways	06/2011	06/2013	06/2013	600.00	600.00
120	VARANASI-AURANGABAD KM.786 TO KM.978.40	Road Transport & Highways	09/2011	03/2014	03/2014	2848.00	2848.00
121	4-LANNING OF CHAPRA-HAJIPUR	Road Transport & Highways	01/2011	07/2013	07/2013	575.00	575.00
122	SRINAGAR TO BANIHAL	Road Transport & Highways	06/2011	06/2014	06/2014	1100.70	1100.70
123	BHUBANESWAR TO PURI	Road Transport & Highways	03/2011	08/2013	08/2013	500.29	500.29
124	4-laning of Raiganj-Dalkola	Road Transport & Highways	02/2011	08/2013	08/2013	580.43	580.43
125	6-LANING OF DHANKUNI-KHARAGPUR SECTION	Road Transport & Highways	04/2012	09/2014	09/2014	1396.18	1396.18
126	2 LANING WITH PS KANPUR KABRAI	Road Transport & Highways	01/2013	07/2014	07/2014	373.47	373.47
127	AHMEDABAD TO VADODARA SECTION	Road Transport & Highways	01/2013	12/2015	12/2015	2125.24	2125.24
128	Talegaon-amravati	Road Transport & Highways	11/2009	11/2013	11/2013	567.00	567.00
129	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	Road Transport & Highways	09/2011	12/2013	12/2013	1250.00	1250.00
130	Two laning of Trichy - Karaikudi and Trychi Bypass	Road Transport & Highways	05/2010	05/2013	05/2013	374.00	374.00

SN	PROJECT	SECTOR	DOA	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED
131	NIROLI-ROXY-RAJAMUNDA	Road Transport & Highways	07/2011	01/2014	01/2014	586.00	586.00
132	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER	Road Transport & Highways	11/2011	05/2014	05/2014	909.00	909.00
133	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	Road Transport & Highways	07/2012	01/2014	01/2014	291.36	291.36
134	4-laning of Faraka-Raiganj	Road Transport & Highways	02/2011	08/2013	08/2013	1078.84	1078.84
135	2 LANNING OF MUZAFFARPUR - SONBARSA	Road Transport & Highways	05/2011	11/2013	11/2013	511.54	511.54
136	2-LANNING WITH PS MOTIHARI-RAXAUL	Road Transport & Highways	10/2011	04/2014	04/2014	375.09	375.09
137	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	Road Transport & Highways	09/2011	03/2014	03/2014	574.00	574.00
138	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	Road Transport & Highways	11/2011	05/2014	05/2014	1535.00	1535.00
139	JORBAT - BARAPANI	Road Transport & Highways	01/2011	01/2014	01/2014	536.00	536.00
140	Tirupati - Tiruthani - Chennai	Road Transport & Highways	04/2011	10/2013	10/2013	571.00	571.00
141	2 Laning of Muzaffarpur - Sonbarsa	Road Transport & Highways	05/2011	11/2013	11/2013	511.54	511.54
142	GHAZIABAD-ALIGARH NH-91	Road Transport & Highways	02/2011	08/2013	08/2013	1141.00	1141.00
143	FOUR LANING OF ORISSA CHATTISHGARH BORDER	Road Transport & Highways	02/2013	08/2015	08/2015	1232.00	1232.00
144	Setting up of Single Point Mooring (SPM) and allied facilities off Veera in Gulf of Kutch on BOT bas	Shipping & Ports	02/2011	05/2013	05/2013	830.00	621.53
145	Acquisition of two(2) Nos. of 317000 DWT very large crude carriers from M/S Jiangsu rongsheng heavy	Shipping & Ports	10/2010	02/2014	02/2014	966.46	994.82
146	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Oddisha	Steel	01/2012	12/2014	12/2014	254.90	254.90
147	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, chattisgarh	Steel	07/2012	08/2014	08/2014	332.65	332.65
148	DELHI MRTS PHASE-III	Urban Development	09/2011	03/2016	03/2016	35242.00	35242.00
149	FARIDABAD EXTENSION	Urban Development	09/2011	09/2014	09/2014	2494.00	2494.00
TOTAL						253987.27	253546.91

LIST OF DELAYED PROJECTS W.R.T. ORIGINAL

SN	PROJECT	SECTOR	DOA	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	TOR IN MONTHS
1	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4	Atomic Energy	10/2009	12/2015	11/2016	11459.00	11459.00	11
2	RAJASTHAN ATOMIC POWER PROJECT -7 and 8 (2X700 MW)	Atomic Energy	10/2009	12/2016	03/2017	12320.00	12320.00	3
3	Construction of New International Terminal Building(Goa)	Civil Aviation	05/2010	05/2012	06/2013	335.61	335.61	13
4	C/o new Airport at Pakyong(Sikkim) Airport	Civil Aviation	01/2009	01/2011	12/2013	309.46	309.46	35
5	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	Coal	10/2004	06/2009	01/2014	2030.78	3027.59	55
6	KRISHNASHILA (NCL) (4MTY)	Coal	06/2011	03/2013	03/2014	789.88	741.62	12
7	TUTICORIN THERMAL POWER PROJECT- 2X500 MW	Coal	05/2008	03/2012	03/2014	4904.54	4909.54	24
8	ANANTA OC EXPANSION PH-III (15.0 Mty)	Coal	08/2008	03/2012	03/2014	207.28	207.28	24
9	ASHOK EXPN.OCP -CCL (10 MTY)	Coal	12/2007	03/2011	03/2014	471.66	341.63	36
10	KULDA OCP (MAHANADI COALFIELDS LTD)	Coal	01/2005	03/2010	03/2014	302.96	302.96	48
11	ADRIYALA SHAFT PROJECT	Coal	12/2009	03/2013	07/2014	212.34	977.53	16
12	KANIHA OCP, MCL, (10.0 Mty)	Coal	12/2007	03/2013	03/2015	457.77	457.77	24
13	HINGULA OC-II EXP. PH-III (15 MTY)	Coal	11/2008	03/2013	03/2015	479.63	479.63	24
14	Purnadih OCP (3.0 MTY)	Coal	07/2008	03/2013	03/2015	210.98	210.98	24
15	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	Coal	10/2007	03/2012	03/2015	259.40	259.40	36
16	RAMAGUNDAM OC-II EXTENSION	Coal	12/2009	03/2012	03/2015	418.97	418.97	36
17	MANUGURU OC-II EXTENSION PHASE-II	Coal	03/2010	03/2012	03/2015	181.19	181.19	36
18	BALRAM OCP EXTENSION,MCL 8.00 Mty	Coal	12/2007	03/2010	03/2015	172.08	172.08	60
19	GEVRA EXPANSION OCP (SECL) (25-35) MTY	Coal	06/2010	03/2014	03/2016	2675.67	2675.67	24
20	DIPKA EXPANSION OCP (SECL) (20-25) MTY	Coal	12/2009	03/2014	03/2016	1943.66	1943.66	24
21	CHURCHA ROUG(1.35MTY)	Coal	06/2008	03/2014	03/2016	462.35	462.35	24
22	RAJMAHAL OC EXP.	Coal	09/2009	03/2014	03/2016	153.82	153.82	24
23	PENGANGA OC	Coal	10/2008	03/2014	03/2016	339.77	339.77	24
24	KARTALI (EAST) OCP (2.50 MTY)	Coal	07/2008	03/2014	03/2016	178.44	178.44	24
25	MANIKPUR OC EXPANSION (3.5 MTY)	Coal	12/2009	03/2014	03/2016	321.42	321.50	24
26	KAKATIYA LONGWALL	Coal	12/2008	12/2012	03/2016	453.63	453.63	39
27	MAGADH OC 20 MTY (CCL)	Coal	08/2008	07/2012	03/2016	469.78	706.40	44

SN	PROJECT	SECTOR	DOA	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	TOR IN MONTHS
28	Tapin OCP (2.5 MTY)	Coal	08/2008	03/2012	03/2016	264.68	264.68	48
29	Churi Benti UG (0.81 MTY)	Coal	08/2007	03/2011	03/2016	163.51	163.51	60
30	JAGANNATHPOR OC	Coal	09/2008	03/2015	03/2017	152.43	152.43	24
31	North Urimari OCP (3.0 MTY)	Coal	12/2007	03/2012	03/2017	179.87	179.87	60
32	JHANJRA R-VI SEAM PSLW	Coal	11/2006	03/2011	03/2017	287.18	287.17	72
33	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW)	Coal	06/2011	12/2015	12/2017	5907.11	5907.11	24
34	Assam gas Cracker project	Petrochemicals	04/2006	04/2012	12/2013	5460.61	8920.00	20
35	MRPL Phase-III Expansion	Petroleum	08/2008	01/2012	05/2013	12412.00	12160.26	16
36	North Tapti Gas Field Development	Petroleum	07/2008	03/2011	05/2013	589.70	973.79	26
37	DEVELOPMENT OF B-46 CLUSTER FIELD	Petroleum	06/2007	07/2010	05/2013	1436.21	1436.21	34
38	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH	Petroleum	01/2007	03/2010	05/2013	740.02	740.02	38
39	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY	Petroleum	04/2008	04/2013	06/2013	825.00	1827.00	2
40	Development of BHE and BH-35 Area.	Petroleum	08/2010	03/2013	06/2013	372.11	372.11	3
41	Butadiene Extraction Unit(BDEU) at Panipat	Petroleum	11/2009	02/2013	06/2013	341.50	341.50	4
42	Up-gradation of Konaban GGS and Pipeline Grid Project, Tripura	Petroleum	07/2008	08/2012	06/2013	288.04	253.66	10
43	ADDITIONAL DEV. OF D-1 FIELD	Petroleum	01/2010	06/2012	06/2013	2163.64	2163.64	12
44	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT	Petroleum	08/2009	04/2012	06/2013	246.81	276.83	14
45	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY	Petroleum	03/2009	09/2011	06/2013	3597.00	2730.00	21
46	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY	Petroleum	03/2009	09/2011	06/2013	3284.00	2174.00	21
47	DEVELOPMENT OF B-22 CLUSTER FIELDS	Petroleum	01/2007	09/2010	06/2013	2323.40	2920.82	33
48	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2	Petroleum	10/2007	05/2010	06/2013	5713.03	8813.41	37
49	DEVELOPMENT OF C-SERIES FIELDS	Petroleum	08/2006	12/2008	06/2013	3195.16	3690.37	54
50	DEV OF G1 AND GS-15 (ONGCL)	Petroleum	04/2003	04/2006	06/2013	429.82	2735.65	86
51	IOR, RUDRASAGAR (ONGCL)	Petroleum	09/2001	03/2006	06/2013	113.90	438.85	87
52	ADDITIONAL GAS PROCESSING UNITS AT URAN	Petroleum	10/2008	12/2011	07/2013	1797.35	977.00	19
53	Fluidized catalytic cracking unit(FCCU) revamp at Mathura Refinery	Petroleum	07/2010	01/2013	09/2013	1000.00	1000.00	8

SN	PROJECT	SECTOR	DOA	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	TOR IN MONTHS
54	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II	Petroleum	01/2009	09/2012	09/2013	7133.39	6855.93	12
55	Construction of 6 ETPs	Petroleum	03/2009	09/2012	09/2013	302.26	240.95	12
56	Development of SB-14 field	Petroleum	01/2011	11/2012	10/2013	410.44	410.44	11
57	Polypropylene unit	Petroleum	05/2009	07/2012	10/2013	1803.78	1803.78	15
58	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	Petroleum	03/2011	05/2013	11/2013	861.79	761.68	6
59	Construction of one Multipurpose Support Vessel (MSV)	Petroleum	01/2010	03/2013	11/2013	723.64	723.64	8
60	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG	Petroleum	01/2006	10/2011	12/2013	672.00	1038.00	26
61	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	Petroleum	01/2006	10/2011	12/2013	732.00	1227.00	26
62	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	Petroleum	06/2007	09/2011	12/2013	736.65	736.65	27
63	DEVELOPMENT OF B-193 CLUSTER FIELDS	Petroleum	06/2007	08/2010	12/2013	3248.78	5633.44	40
64	Construction of 23 Immediate Supply Vessels (ISV)	Petroleum	11/2010	08/2013	01/2014	331.20	269.10	5
65	ASSAM RENEWAL PROJECT FOR GROUP A	Petroleum	03/2009	03/2013	03/2014	2465.15	2378.86	12
66	PARADIP REFINERY PROJECT	Petroleum	02/2009	11/2012	03/2014	29777.00	32710.00	16
67	102 MW WIND POWER PROJECT	Petroleum	07/2010	06/2012	03/2014	1106.00	678.02	21
68	IOR LAKWA - LAKHMANI (ONGCL)	Petroleum	09/2001	03/2007	03/2014	345.10	663.69	84
69	IOR of B-173A Field	Petroleum	01/2012	03/2014	04/2014	352.49	352.49	1
70	Development of Cluster-7 Fields	Petroleum	03/2010	03/2013	04/2014	3241.03	5916.65	13
71	JHAJJAR HISSAR PIPE LINE PROJECT	Petroleum	11/2007	10/2010	12/2014	281.07	281.07	50
72	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE	Petroleum	08/2011	07/2015	08/2015	586.00	586.00	1
73	Integrated Refinery Expansion Project	Petroleum	01/1999	12/2015	05/2016	14225.00	14225.00	5
74	IOR GELEKI (ONGCL)	Petroleum	09/2001	03/2007	03/2017	390.09	1674.11	120
75	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC)	Power	10/2003	03/2007	04/2013	768.92	1628.00	73

SN	PROJECT	SECTOR	DOA	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	TOR IN MONTHS
76	INTERCONNECTION BETWEEN ELECTTRICAL GRIDS OF INDIA AND BANGLADESH -INDIAN PORTION	Power	10/2010	10/2012	05/2013	160.32	160.32	7
77	765KV System for Central part of Northern Region Grid - Part-II	Power	07/2009	06/2012	05/2013	1736.36	1736.36	11
78	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PART-I	Power	02/2009	02/2012	05/2013	1347.32	1347.32	15
79	URI H.E.P STAGE -II (NHPC)	Power	08/2005	11/2009	05/2013	1729.29	2081.00	42
80	System Strengthening -XII of SR	Power	02/2010	06/2012	06/2013	232.34	232.34	12
81	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP	Power	07/2006	01/2010	06/2013	557.24	758.75	41
82	Supplementary transmission associated with vellur TPS	Power	08/2010	04/2013	09/2013	170.36	170.36	5
83	NORTHERN REGION SYSTEM STRENGHTENING SCHEME-XX	Power	10/2010	01/2013	09/2013	182.68	182.68	8
84	765KV System for Central part of Northern Region Grid - Part-III	Power	11/2009	05/2012	09/2013	1075.12	1075.12	16
85	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP	Power	02/2009	11/2011	09/2013	184.19	184.19	22
86	EASTERN REGION STRENGTHENING SCHEME-I	Power	10/2006	10/2009	09/2013	975.96	975.96	47
87	NIMOO BAZGO HYDROELECTRIC PROJECT	Power	08/2006	08/2010	10/2013	611.01	936.00	38
88	RIHAND STTP STAGE-III (2X500MW)	Power	01/2009	10/2012	11/2013	6230.81	6230.81	13
89	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA MEGA POWER PROJECT	Power	12/2008	12/2012	12/2013	7031.88	7031.88	12
90	NORTHERN REGION SYSTEM STRENGHTENING SCHEME-XIX	Power	02/2009	02/2012	12/2013	410.29	410.29	22
91	NORTHERN REGION SYSTEM STRENGHTENING SCHEME-XVIII	Power	02/2009	11/2011	12/2013	509.66	509.66	25
92	Transmission system for phase-I generation projects in orissa-part B	Power	12/2010	12/2013	03/2014	2743.19	2743.19	3
93	Northern region system strenghening scheme XVI	Power	07/2010	07/2013	03/2014	752.64	752.64	8

SN	PROJECT	SECTOR	DOA	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	TOR IN MONTHS
94	Northern region system strengthening scheme-XXI	Power	08/2010	04/2013	03/2014	1677.57	1677.57	11
95	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A	Power	09/2010	03/2013	03/2014	2074.86	2074.86	12
96	Trans. System associated with PALLATANA GBPP & BPTS.	Power	02/2010	12/2012	03/2014	2144.00	2144.00	15
97	Northern Region Transmission Strengthening Scheme	Power	03/2010	11/2012	03/2014	965.58	965.58	16
98	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	Power	10/2008	10/2012	03/2014	4824.12	4824.12	17
99	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC	Power	08/2008	08/2012	03/2014	2360.95	2360.95	19
100	765 KV POOLING STATION AND NETWORK WITH DVC AND MAITHOB RBC	Power	08/2008	08/2012	03/2014	7075.33	7075.33	19
101	RAMPUR HEP(412 MW)	Power	01/2007	01/2012	03/2014	2047.03	2047.03	26
102	PARBATI H.E.P. STAGE -III (NHPC)	Power	10/2005	10/2010	03/2014	2304.56	2716.00	41
103	TEESTA LOW DAM HEP, STAGE-IV (NHPC)	Power	09/2005	09/2009	05/2014	1061.38	1501.75	56
104	System Strengthening in NR for SASAN & MUNDRA (UMPP)	Power	12/2009	08/2012	06/2014	1216.83	1216.83	22
105	NORTHERN REGION SYSTEM STRENGHTENING SCHEME-XV	Power	02/2009	11/2011	07/2014	520.48	520.48	32
106	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1	Power	10/2011	11/2013	09/2014	558.26	558.26	10
107	BARH STPP STAGE -II	Power	02/2008	08/2013	09/2014	7341.04	7341.04	13
108	EASTERN REGION TRANSMISSION SYSTEM-III	Power	07/2010	11/2012	09/2014	1272.80	1272.80	22
109	PARE HYDRO ELECTRIC PROJECT	Power	12/2008	08/2012	09/2014	573.99	573.99	25
110	KOLDAM HEP (NTPC)	Power	10/2002	04/2009	09/2014	4527.15	6358.91	65
111	Transmission system for transfer of power from Gen.proj in sikkim to NR/WR part-B	Power	03/2011	11/2013	12/2014	1585.12	1585.12	13
112	Transmission system for transfer of power from Gen.proj in sikkim to NR/WR part-A	Power	05/2010	01/2013	12/2014	250.03	250.03	23

SN	PROJECT	SECTOR	DOA	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	TOR IN MONTHS
113	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	Power	01/2011	07/2014	02/2015	913.63	913.63	7
114	Transmission System of Vindhuachal -IV & Rihand -III Gen. Proj.	Power	03/2010	11/2012	03/2015	4672.99	4672.99	28
115	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII	Power	09/2012	04/2015	05/2015	524.40	524.40	1
116	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	Power	02/2009	08/2013	06/2015	11130.19	11130.19	22
117	BONGAIGAON THERMAL POWER PROJECT	Power	01/2008	07/2011	10/2015	4375.35	4375.35	51
118	Tapovan-Vishnugad HEP (4x130MW)	Power	11/2006	03/2013	03/2016	2978.48	2978.48	36
119	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	Power	08/2008	07/2014	05/2016	2491.58	3422.44	22
120	KISHANGANGA HEP	Power	07/2007	01/2016	11/2016	2238.67	3642.00	10
121	TEHRI PUMPED STORAGE PLANT(1000MW)	Power	07/2006	07/2010	11/2016	1657.00	2978.86	76
122	BARH STPP(3X660MW) NTPC	Power	12/2003	12/2009	02/2017	8692.97	8693.00	86
123	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	Power	12/2004	05/2013	03/2017	2496.90	2496.90	46
124	SUBANSIRI LOWER H.E.P (NHPC)	Power	09/2003	09/2010	12/2017	6285.33	10667.00	87
125	PARBATI HEP (NHPC) II	Power	09/2002	09/2009	03/2018	3919.59	5366.00	102
126	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	04/1993	03/2002	07/2013	100.00	227.94	136
127	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	Railways	04/1999	12/2009	10/2013	108.00	432.72	46
128	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR)	Railways	04/1986	03/1994	10/2013	158.77	580.83	235
129	Ghutiasharif-Canning (ER)	Railways	04/2009	12/2011	11/2013	189.97	611.03	23
130	Bandel-Naihati new rail bridge in replacement of jubilee bridge no.8 (ER)	Railways	04/1999	12/2012	12/2013	207.52	207.52	12
131	Ramanagram-Mysore doubling with electrification of Kengesii- Musore (SWR)	Railways	04/2007	03/2013	03/2014	482.00	482.70	12
132	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BAD-MEERUT	Railways	02/2008	03/2012	03/2014	171.10	246.44	24
133	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	Railways	04/2000	03/2009	08/2014	133.41	276.00	65
134	RAJATGARH-BARANG(LD),ECOR	Railways	04/1999	02/2009	08/2014	166.16	288.00	66

SN	PROJECT	SECTOR	DOA	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	TOR IN MONTHS
135	ETAWAH-MAINPURI (NL),NCR	Railways	09/2001	12/2008	09/2014	129.70	245.39	69
136	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	Railways	04/2006	06/2013	12/2014	495.74	495.74	18
137	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR	Railways	04/2002	03/2009	12/2014	921.00	2363.00	69
138	Katakhal to Bhairabi	Railways	04/1998	12/2012	03/2015	227.90	223.01	27
139	KATIHAR - JOGBANI (GC)(NEFR)	Railways	09/2001	12/2010	03/2015	100.00	1041.79	51
140	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project	Railways	04/1996	03/2009	03/2015	1676.31	4255.37	72
141	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	Railways	04/2000	12/2008	03/2015	733.00	1655.81	75
142	HOWRAH-AMTA-CHAMPADANGA NL (SER)	Railways	04/1974	03/2007	03/2015	31.42	535.40	96
143	AGARTALA SABROOM, NL, NEFR	Railways	04/2008	03/2014	12/2015	813.34	1141.75	21
144	BHOPAL BINA 3D LINE DOUBLING	Railways	09/2007	03/2010	12/2015	687.20	800.00	69
145	PANSPURA-KHARAGPUR 3D LINE	Railways	09/2007	02/2010	12/2015	252.50	529.23	70
146	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR	Railways	09/1997	04/2008	12/2015	1000.00	4996.65	92
147	PATNA GANGA BRIDGE (NL), ECR	Railways	04/2001	10/2007	12/2015	624.47	2921.00	98
148	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	Railways	03/1996	03/2004	03/2016	401.81	1512.86	144
149	New Work for Construction of Metro railway from Noapara-Barasai VIA Bimanbander (MTP)	Railways	04/2010	03/2016	06/2016	2397.72	2397.72	3
150	TAMLUK DIGHA,LINE DOUBLING (SER)	Railways	03/1984	06/2005	06/2016	293.97	1074.47	132
151	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	Railways	04/2008	03/2014	12/2016	5300.00	5300.00	33
152	BANKURA - DAMODAR (GC) (SER)	Railways	03/1998	03/2005	12/2016	111.90	1423.98	141
153	SEVOK RANGPO, NEFR	Railways	04/2008	12/2015	03/2017	1339.48	3380.58	15
154	New Line from Dimapur to Zubza(Kohima) national project (NEFR)	Railways	04/2006	03/2015	03/2017	850.00	2446.81	24
155	BHAIRABI SAIRONG, NL, NEFR	Railways	04/2008	04/2014	03/2017	619.34	2384.34	35
156	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	Railways	04/2003	03/2011	03/2017	727.56	4453.50	72
157	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	Railways	04/2006	03/2010	03/2017	325.00	819.40	84
158	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	03/2001	12/2017	2500.00	20000.00	201

SN	PROJECT	SECTOR	DOA	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	TOR IN MONTHS
159	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68	Road Transport & Highways	03/2005	01/2011	05/2013	941.00	941.00	28
160	GWALIOR BYPASS, NH-75,3	Road Transport & Highways	12/2003	10/2009	05/2013	300.93	300.93	43
161	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	Road Transport & Highways	12/2003	09/2008	05/2013	332.94	332.94	56
162	NAGAON TO DHARAMTUL (AS-2)	Road Transport & Highways	12/2003	06/2008	05/2013	264.72	264.72	59
163	DHARAMTUL TO SONAPUR (AS-19)	Road Transport & Highways	12/2003	06/2008	05/2013	200.00	200.00	59
164	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0	Road Transport & Highways	12/2003	03/2008	05/2013	340.68	340.68	62
165	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5)	Road Transport & Highways	04/2000	04/2004	05/2013	225.00	241.53	109
166	GANJAM-ICCHAPURUM,NH-5(NHAI)	Road Transport & Highways	04/2000	02/2004	05/2013	263.27	263.27	111
167	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5	Road Transport & Highways	04/2000	02/2004	05/2013	228.70	228.70	111
168	Hazaribagh-Ranchi	Road Transport & Highways	08/2010	01/2013	06/2013	625.07	625.07	5
169	Jaipur-Tonk-Deoli	Road Transport & Highways	06/2010	12/2012	06/2013	792.06	792.06	6
170	AMRITSAR-PATHANKOT	Road Transport & Highways	05/2010	11/2012	06/2013	705.00	705.00	7
171	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	Road Transport & Highways	03/2005	07/2012	06/2013	940.00	940.00	11
172	Kishangarh-Ajmer-Beawer	Road Transport & Highways	11/2009	05/2012	06/2013	795.00	795.00	13
173	Armur to kadloor yellareddy	Road Transport & Highways	02/2010	02/2012	06/2013	390.56	390.56	16
174	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.15)	Road Transport & Highways	05/2009	10/2011	06/2013	572.30	572.30	20
175	Surat- Dahisar(Six Lane) Km 263 to Km 502	Road Transport & Highways	02/2009	08/2011	06/2013	1693.75	1693.75	22
176	NEW MANGALORE PORT NH-17 AND 48	Road Transport & Highways	04/2000	06/2011	06/2013	196.50	196.50	24

SN	PROJECT	SECTOR	DOA	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	TOR IN MONTHS
177	DELHI/ HARYANA BORDER TO ROHTAK	Road Transport & Highways	04/2007	05/2010	06/2013	486.00	486.00	37
178	JHANSI TO LALITPUR, NH-25,26	Road Transport & Highways	12/2003	09/2009	06/2013	355.06	355.06	45
179	THANJAUR-TRICHY,NH-67(NHAI)	Road Transport & Highways	03/2005	06/2009	06/2013	280.00	280.00	48
180	NAGPUR-KONDHALI,NH-6(NHAI)	Road Transport & Highways	03/2005	12/2008	06/2013	168.00	168.00	54
181	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI)	Road Transport & Highways	12/2003	10/2008	06/2013	251.03	251.03	56
182	SONAPUR TO GUWAHTI (AS-3)	Road Transport & Highways	12/2003	03/2008	06/2013	245.00	245.00	63
183	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4)	Road Transport & Highways	04/2000	08/2004	06/2013	241.00	196.65	106
184	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4)	Road Transport & Highways	04/2000	08/2004	06/2013	318.00	207.56	106
185	JAIPUR-REENGUS	Road Transport & Highways	08/2010	02/2013	07/2013	267.81	267.81	5
186	GWALIOR-JHANSI, NH-75	Road Transport & Highways	12/2003	12/2009	07/2013	604.00	604.00	43
187	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	Road Transport & Highways	09/2010	03/2013	08/2013	852.00	852.00	5
188	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km)	Road Transport & Highways	05/2009	11/2011	08/2013	1108.00	2288.00	21
189	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM	Road Transport & Highways	11/2010	05/2013	09/2013	1585.00	1585.00	4
190	KOTA BYPASS,RJ-4, NH-76 (NHAI)	Road Transport & Highways	12/2003	10/2008	09/2013	275.00	250.39	59
191	NALBARI TO BIJNI (AS-8)	Road Transport & Highways	12/2003	06/2008	09/2013	200.00	200.00	63
192	NALBARI TO BIJNI (AS-6)	Road Transport & Highways	12/2003	06/2008	09/2013	225.00	225.00	63
193	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A	Road Transport & Highways	12/2003	05/2008	09/2013	284.00	359.00	64

SN	PROJECT	SECTOR	DOA	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	TOR IN MONTHS
194	PATNA-MUZZAFFARPUR	Road Transport & Highways	08/2010	02/2013	10/2013	671.30	671.30	8
195	BHOPAL-SANCHI	Road Transport & Highways	10/2011	01/2013	10/2013	209.00	209.00	9
196	Pune-sholapur, pkg1	Road Transport & Highways	11/2009	05/2012	10/2013	1110.00	1110.00	17
197	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24	Road Transport & Highways	03/2005	09/2007	11/2013	220.00	220.00	74
198	SAMAIKHIALI - GANDHIDHAM	Road Transport & Highways	09/2010	03/2013	12/2013	805.39	805.39	9
199	Gujarat/Maharashtra Border Surat-Hazira Port Section	Road Transport & Highways	03/2010	09/2012	12/2013	1509.10	1509.10	15
200	Gurgaon-Kotputli Km 42.70 to 54.4 Km	Road Transport & Highways	04/2009	10/2011	12/2013	1673.70	1673.70	26
201	Four Lanning from MP/Maharashtra Border to nagpur, Nagpur bypass	Road Transport & Highways	04/2010	06/2011	12/2013	1170.52	1170.52	30
202	LAKHNAADON TO MP/MH BORDER, KM 596.75-653.22 (NS-1/BOT/MP-2), NH7	Road Transport & Highways	12/2003	06/2010	12/2013	407.60	407.60	42
203	AURANG-RAIPUR, NH-6, KM.232 TO KM.281	Road Transport & Highways	03/2005	01/2009	12/2013	190.00	190.00	59
204	KOTWA TO DEWAPUR(10 LMNHP), NH-28 PHASE-II, KM.440 TO KM.402	Road Transport & Highways	12/2003	10/2008	12/2013	240.00	240.00	62
205	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	Road Transport & Highways	12/2003	05/2008	12/2013	160.00	160.00	67
206	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	Road Transport & Highways	12/2003	09/2007	12/2013	157.47	154.57	75
207	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	Road Transport & Highways	12/2003	09/2010	01/2014	232.45	232.45	40
208	INDORE-DEWAS(NH-3)	Road Transport & Highways	11/2010	05/2013	02/2014	325.00	325.00	9
209	HARIDWAR-DEHRADUN (APPROVED LENGTH 69)	Road Transport & Highways	11/2011	10/2013	03/2014	478.00	478.00	5
210	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION	Road Transport & Highways	04/2011	10/2013	03/2014	682.00	682.00	5
211	2 LANNING OF MOKAMA-MUNGER	Road Transport & Highways	05/2011	05/2013	03/2014	351.54	351.54	10

SN	PROJECT	SECTOR	DOA	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	TOR IN MONTHS
212	MUZAFFARNAGAR-HARIDWAR	Road Transport & Highways	09/2011	03/2013	03/2014	754.00	754.00	12
213	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM)	Road Transport & Highways	02/2011	11/2012	03/2014	193.45	193.45	16
214	Chennai-Tada(Six lane)	Road Transport & Highways	04/2009	10/2011	03/2014	353.37	353.37	29
215	TRICHY - KORUR NH-67	Road Transport & Highways	03/2005	07/2010	03/2014	516.00	516.00	44
216	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06	Road Transport & Highways	12/2003	09/2008	03/2014	155.00	201.66	66
217	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	Road Transport & Highways	12/2003	06/2008	03/2014	195.00	195.00	69
218	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	Road Transport & Highways	12/2003	06/2008	03/2014	237.80	237.80	69
219	GUWHATI TO NALBARI (AS-4)	Road Transport & Highways	12/2003	04/2008	03/2014	175.96	175.96	71
220	GUWAHATI TO NALBARI (AS-5)	Road Transport & Highways	12/2003	04/2008	03/2014	198.16	198.16	71
221	AGRA-BYPASS(NS-1/UP-1), NH-2,3	Road Transport & Highways	12/2003	09/2007	03/2014	348.16	465.50	78
222	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C	Road Transport & Highways	12/2003	06/2005	03/2014	230.00	230.00	105
223	2-LANNING WITH PS KHAGARIA-PURNEA	Road Transport & Highways	05/2011	02/2014	04/2014	664.00	664.00	2
224	PUNE-SATARA(NH-4)	Road Transport & Highways	10/2010	03/2013	04/2014	1724.55	1724.55	13
225	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54	Road Transport & Highways	12/2003	09/2007	04/2014	212.00	386.10	79
226	HARANGAJO TO MAIBANG, NH-54	Road Transport & Highways	12/2003	07/2009	05/2014	196.00	363.74	58
227	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	Road Transport & Highways	12/2003	02/2009	05/2014	280.00	280.00	63
228	NALBARI T BIJNI (AS-7)	Road Transport & Highways	12/2003	04/2008	05/2014	208.00	208.00	73
229	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	Road Transport & Highways	07/2010	07/2013	06/2014	1813.76	1813.76	11

SN	PROJECT	SECTOR	DOA	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	TOR IN MONTHS
230	Kandla - Mundra port	Road Transport & Highways	01/2011	07/2013	06/2014	953.88	953.88	11
231	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450	Road Transport & Highways	12/2003	11/2008	06/2014	155.04	280.13	67
232	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915	Road Transport & Highways	12/2003	10/2008	06/2014	300.00	300.00	68
233	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER	Road Transport & Highways	03/2011	09/2013	07/2014	359.00	359.00	10
234	LUCKNOW-RAIBAREILI	Road Transport & Highways	07/1999	07/2012	07/2014	635.90	635.90	24
235	CHAMBAL BRIDGE, NH-76 (RJ-5)	Road Transport & Highways	12/2003	02/2010	07/2014	275.00	281.31	53
236	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7	Road Transport & Highways	12/2003	09/2009	09/2014	263.17	263.17	60
237	BRAHMPUTRA BRIDGE,NH NO-31	Road Transport & Highways	12/2003	04/2010	11/2014	217.61	217.61	55
238	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	Road Transport & Highways	03/2005	02/2010	12/2014	557.00	557.00	58
239	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000	Road Transport & Highways	12/2003	04/2009	12/2014	199.81	385.13	68
240	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500	Road Transport & Highways	12/2003	04/2009	12/2014	200.00	200.00	68
241	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54	Road Transport & Highways	12/2003	11/2008	12/2014	167.64	167.64	73
242	2 laning of Dindigul - Perigulam Theni- kumili	Road Transport & Highways	09/2011	08/2013	02/2015	485.00	485.00	18
243	SIX LANNING OF VADAKKANCHERRY THRISSURE SECTION(KM 240-270KM)	Road Transport & Highways	02/2010	08/2012	03/2015	617.00	617.00	31
244	4 LANING OF NAGPUR-BETUL	Road Transport & Highways	02/2011	08/2014	07/2015	2498.76	2498.76	11
245	NASHRI CHANANI	Road Transport & Highways	06/2010	06/2015	05/2016	2159.00	2159.00	11
246	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	Road Transport & Highways	07/2010	07/2015	06/2016	1987.00	1987.00	11

SN	PROJECT	SECTOR	DOA	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	TOR IN MONTHS
247	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER	Shipping & Ports	07/2011	01/2013	06/2013	220.49	220.49	5
248	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	Shipping & Ports	10/2002	03/2006	06/2013	150.00	600.00	87
249	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN	Shipping & Ports	03/2009	01/2012	07/2013	3500.00	4150.00	18
250	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY VESSELS	Shipping & Ports	10/2007	04/2011	09/2013	359.44	359.44	29
251	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers from M/S Jiangsu Eastern Heavy Industries	Shipping & Ports	08/2010	12/2012	10/2013	612.72	532.83	10
252	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL	Shipping & Ports	11/2007	12/2010	04/2014	1228.00	1460.00	40
253	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY	Shipping & Ports	01/2012	03/2014	08/2014	511.87	511.87	5
254	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREMENT EXP. UNIT	Steel	07/2007	02/2011	04/2013	230.00	343.58	26
255	330 TPH BOILER-6 AND AUXILIARY SYSTEM	Steel	07/2007	08/2010	04/2013	260.00	350.00	32
256	COKE OVEN BATTERY NO. 4 PHASE-II	Steel	08/2007	10/2012	06/2013	108.00	216.68	8
257	Augmentation of Iron Ore Storage in RMHP	Steel	05/2008	05/2012	06/2013	480.00	450.00	13
258	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	Steel	10/2005	10/2009	06/2013	8692.00	12291.00	44
259	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC)	Steel	02/2011	05/2013	11/2013	898.55	898.55	6
260	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC)	Steel	04/2011	04/2013	12/2013	572.00	572.00	8
261	Expansion of Rourkela Steel Plant	Steel	09/2008	03/2013	12/2013	11812.00	11812.00	9
262	EXPANSION OF DURGAPUR STEEL PLANT	Steel	06/2009	12/2012	12/2013	2875.00	2875.00	12
263	Bailadila Iron Ore Project Deposit- 11B (NMDC)	Steel	01/2007	12/2011	12/2013	295.89	607.17	24
264	EXPANSION OF IISCO STEEL PLANT	Steel	02/2008	12/2011	12/2013	14443.00	16408.00	24
265	EXPANSION OF BOKARO STEEL PLANT	Steel	01/2008	12/2011	12/2013	6325.00	6325.00	24
266	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES	Steel	11/2011	11/2013	03/2014	254.55	254.55	4

SN	PROJECT	SECTOR	DOA	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	TOR IN MONTHS
267	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES	Steel	12/2011	10/2013	03/2014	187.33	187.33	5
268	EXPANSION OF BHILAI STEEL PLANT	Steel	09/2008	03/2013	03/2014	17265.00	17265.00	12
269	GSM equipment of 1625000Lines (2G) 325000 lines 3(G) MP Phase V.1 Telecom Circle	Telecommunications	11/2009	11/2010	06/2013	916.70	916.70	31
270	Supply Installation testing and commissioning of Rural Wimax network Phase-II	Telecommunications	07/2010	05/2011	08/2013	1148.19	964.37	27
271	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL	Telecommunications	01/2009	06/2009	08/2013	149.15	158.72	50
272	Assam Telecom Circle, Phase-V.I, 2G & 3G	Telecommunications	06/2007	01/2009	08/2013	336.81	336.81	55
273	ERP implementation in BSNL on Turnkey basis	Telecommunications	10/2009	10/2010	12/2013	384.00	384.00	38
TOTAL						436822.20	525231.96	

List of Projects in which Expenditure is more than cost

SN	PROJECT	SECTOR	DOC ORIGINAL	COST ORIGINAL	COST REVISED	CUMULATIVE EXPENDITURE
1	KUDANKULAM APP (NPCIL)	Atomic Energy	12/2008	13171.00	0.00	16007.00
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	Atomic Energy	09/2010	3492.00	0.00	4080.48
3	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT	Civil Aviation	05/2011	1942.51	0.00	2462.84
4	RESITMENT OF MARKETING INSTALATION AT VISAKH	Petroleum	N.A.	756.00	898.00	986.69
5	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY	Petroleum	04/2013	825.00	0.00	1433.73
6	KOLDAM HEP (NTPC)	Power	04/2009	4527.15	0.00	4940.00
7	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC)	Power	03/2007	768.92	0.00	1486.94
8	TEESTA LOW DAM HEP, STAGE-IV (NHPC)	Power	09/2009	1061.38	0.00	1116.04
9	NIMOO BAZGO HYDROELECTRIC PROJECT	Power	08/2010	611.01	0.00	730.06
10	CHUTAK HYDRO-ELECTRIC PROJECT	Power	02/2011	621.26	0.00	731.93
11	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP	Power	01/2010	557.24	0.00	638.60
12	RAMPUR HEP(412 MW)	Power	01/2012	2047.03	0.00	2375.16
13	TRIPURA GAS BASED POWER PROJECT	Power	N.A.	421.01	0.00	527.59
14	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	N.A.	124.43	495.68	604.50
15	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/2001	2500.00	2500.00	8877.37
16	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	03/2002	100.00	142.98	221.13
17	CALICUT-MANGALORE (DL) (SR)	Railways	N.A.	240.00	0.00	599.40
18	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR	Railways	N.A.	295.00	412.91	609.63
19	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR)	Railways	03/2012	157.00	262.82	294.00
20	KARUR-SALEM(NL),SR	Railways	N.A.	155.55	155.00	758.16
21	NANDYAL-YERRAGUNTALA(NL),SCR	Railways	02/2009	155.74	429.49	650.87
22	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR	Railways	04/2008	1000.00	1500.00	2724.46
23	KOTTUR-HARIHAR(NL),(SWR)	Railways	N.A.	65.94	302.23	350.13
24	RANCHI-LOHARDAGA(GC),SER	Railways	06/2004	194.07	194.07	326.81

SN	PROJECT	SECTOR	DOC ORIGINAL	COST ORIGINAL	COST REVISED	CUMULATIVE EXPENDITURE
25	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	Railways	03/2012	233.00	501.69	694.03
26	CHANDIGARH-LUDHIANA(NEW BG LINE),NR	Railways	12/2012	248.44	576.27	951.56
27	KATIHAR - JOGBANI (GC)(NEFR)	Railways	12/2010	100.00	492.98	741.88
28	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER)	Railways	N.A.	381.17	381.17	626.57
29	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	Railways	N.A.	323.40	323.40	511.30
30	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	Railways	06/2007	409.00	625.30	841.01
31	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	Railways	N.A.	100.00	100.00	540.49
32	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	Railways	12/2008	733.00	733.00	1372.73
33	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara and Noapara-NSCB Airport(MTP)	Railways	12/2006	907.69	3156.32	3421.35
34	GADWAL - RAICHUR (NL), SCR	Railways	02/2011	92.63	228.09	278.46
35	JIND-SONEPAT (NL),NR	Railways	03/2012	190.81	238.56	441.77
36	RAJATGARH-BARANG(LD),ECOR	Railways	02/2009	166.16	0.00	271.99
37	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	Railways	03/2011	727.56	727.53	1370.28
38	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	Railways	N.A.	915.70	915.70	1787.92
39	RAICHUR-GUNTAKAL(DL)(SCR)	Railways	12/2007	136.62	0.00	257.91
40	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	Railways	03/2012	114.01	332.92	419.92
41	BHOPAL BINA 3D LINE DOUBLING	Railways	03/2010	687.20	0.00	718.89
42	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	Railways	N.A.	343.17	343.17	625.68
43	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	Railways	03/2011	170.00	170.00	396.76
44	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR	Railways	N.A.	156.00	156.00	328.82
45	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project	Railways	03/2009	1676.31	1676.31	3444.56
46	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	Road Transport & Highways	09/2007	157.47	0.00	231.80

SN	PROJECT	SECTOR	DOC ORIGINAL	COST ORIGINAL	COST REVISED	CUMULATIVE EXPENDITURE
47	HAPUR-GARH Mukteswar (Others) KM.58-93, NH-24	Road Transport & Highways	09/2007	220.00	0.00	284.17
48	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C	Road Transport & Highways	06/2005	230.00	0.00	233.72
49	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80	Road Transport & Highways	03/2008	166.27	0.00	193.46
50	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A	Road Transport & Highways	05/2008	284.00	0.00	284.54
51	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402	Road Transport & Highways	10/2008	240.00	0.00	295.65
52	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0	Road Transport & Highways	03/2008	340.68	0.00	400.56
53	AURANG-RAIPUR, NH-6, KM.232 TO KM.281	Road Transport & Highways	01/2009	190.00	0.00	264.27
54	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	Road Transport & Highways	02/2009	280.00	0.00	303.32
55	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	Road Transport & Highways	06/2008	195.00	0.00	232.51
56	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	Road Transport & Highways	06/2008	237.80	0.00	277.43
57	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	Road Transport & Highways	09/2008	332.94	0.00	441.45
58	KOTA BYPASS,RJ-4, NH-76 (NHAI)	Road Transport & Highways	10/2008	275.00	0.00	279.83
59	RAJMARG CHORAH TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI)	Road Transport & Highways	10/2008	251.03	0.00	326.46
60	NALBARI TO BIJNI (AS-8)	Road Transport & Highways	06/2008	200.00	0.00	282.24
61	GUWHATI TO NALBARI (AS-4)	Road Transport & Highways	04/2008	175.96	0.00	182.53
62	NAGAON TO DHARAMTUL (AS-2)	Road Transport & Highways	06/2008	264.72	0.00	299.20
63	SONAPUR TO GUWAHTI (AS-3)	Road Transport & Highways	03/2008	245.00	0.00	491.21
64	GUWAHATI TO NALBARI (AS-5)	Road Transport & Highways	04/2008	198.16	0.00	242.38
65	NALBARI TO BIJNI (AS-6)	Road Transport & Highways	06/2008	225.00	0.00	258.39

SN	PROJECT	SECTOR	DOC ORIGINAL	COST ORIGINAL	COST REVISED	CUMULATIVE EXPENDITURE
66	NALBARI T BIJNI (AS-7)	Road Transport & Highways	04/2008	208.00	0.00	290.59
67	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	Road Transport & Highways	05/2008	160.00	0.00	197.55
68	DHARAMTUL TO SONAPUR (AS-19)	Road Transport & Highways	06/2008	200.00	0.00	246.20
69	NAGPUR-KONDHALI,NH-6(NHAI)	Road Transport & Highways	12/2008	168.00	0.00	457.30
70	THANJAUR-TRICHY,NH-67(NHAI)	Road Transport & Highways	06/2009	280.00	0.00	581.49
71	GANJAM-ICCHAPURUM,NH-5(NHAI)	Road Transport & Highways	02/2004	263.27	0.00	276.26
72	BRAHMPUTRA BRIDGE,NH NO-31	Road Transport & Highways	04/2010	217.61	0.00	258.43
73	GWALIOR BYPASS, NH-75,3	Road Transport & Highways	10/2009	300.93	0.00	303.02
74	JHANSI TO LALITPUR, NH-25,26	Road Transport & Highways	09/2009	355.06	0.00	501.86
75	TRICHY - KORUR NH-67	Road Transport & Highways	07/2010	516.00	0.00	853.94
76	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68	Road Transport & Highways	01/2011	941.00	0.00	1901.00
77	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	Road Transport & Highways	02/2010	557.00	0.00	932.27
78	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	Road Transport & Highways	09/2010	232.45	0.00	295.39
79	DELHI/ HARYANA BORDER TO ROHTAK	Road Transport & Highways	05/2010	486.00	0.00	644.73
80	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	Road Transport & Highways	07/2012	940.00	0.00	1293.20
81	Gujarat/Maharashtra Border Surat-Hazira Port Section	Road Transport & Highways	09/2012	1509.10	0.00	1675.00
82	Pune-sholapur, pkg1	Road Transport & Highways	05/2012	1110.00	0.00	1802.10
83	Kishangarh-Ajmer-Beawer	Road Transport & Highways	05/2012	795.00	0.00	1055.70
84	Chennai-Tada(Six lane)	Road Transport & Highways	10/2011	353.37	0.00	395.08

SN	PROJECT	SECTOR	DOC ORIGINAL	COST ORIGINAL	COST REVISED	CUMULATIVE EXPENDITURE
85	Gurgaon-Kotputli Km 42.70 to 54.4 Km	Road Transport & Highways	10/2011	1673.70	0.00	2777.00
86	Surat- Dahisar(Six Lane) Km 263 to Km 502	Road Transport & Highways	08/2011	1693.75	0.00	2686.20
87	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.15)	Road Transport & Highways	10/2011	572.30	0.00	765.86
88	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km)	Road Transport & Highways	11/2011	1108.00	0.00	3465.90
89	Jaipur-Tonk-Deoli	Road Transport & Highways	12/2012	792.06	0.00	1933.70
90	Hungund-Surathkal and Mangalore-Knt/Kerala Border	Road Transport & Highways	N.A.	946.00	0.00	1485.60
91	Talegaon-amravati	Road Transport & Highways	11/2013	567.00	0.00	891.08
92	Hazaribagh-Ranchi	Road Transport & Highways	01/2013	625.07	0.00	943.25
93	Armur to kadloor yellareddy	Road Transport & Highways	02/2012	390.56	0.00	772.27
94	KUNDUPUR-SURATHKAL & MANGLORE	Road Transport & Highways	N.A.	671.00	0.00	737.54
95	AMRITSAR-PATHANKOT	Road Transport & Highways	11/2012	705.00	0.00	1255.60
96	PANIPAT-ROHTAK	Road Transport & Highways	10/2014	807.00	0.00	1239.30
97	DEVIHALLI-HASSAN	Road Transport & Highways	N.A.	453.00	0.00	524.25
98	MURADABAD-BAREILY	Road Transport & Highways	06/2013	1267.00	0.00	1430.60
99	BELGAUM-DHARWAD(NH-4)	Road Transport & Highways	N.A.	480.00	0.00	488.69
100	INDORE-DEWAS(NH-3)	Road Transport & Highways	05/2013	325.00	0.00	447.50
101	2 LANNING OF MOKAMA-MUNGER	Road Transport & Highways	05/2013	351.54	0.00	392.02
102	4 LANNING OF AHMEDABAD TO GODHARA	Road Transport & Highways	06/2013	1008.50	0.00	1242.30
103	ROHTAK-BAWAL	Road Transport & Highways	11/2013	650.00	0.00	1024.10

SN	PROJECT	SECTOR	DOC ORIGINAL	COST ORIGINAL	COST REVISED	CUMULATIVE EXPENDITURE
104	GHAZIABAD-ALIGARH NH-91	Road Transport & Highways	08/2013	1141.00	0.00	1200.30
105	2 LANNING OF MUZAFFARPUR - SONBARSA	Road Transport & Highways	11/2013	511.54	0.00	579.51
106	4-laning of Barhi-Hazaribagh	Road Transport & Highways	02/2014	398.00	0.00	424.27
107	JAIPUR-REENGUS	Road Transport & Highways	02/2013	267.81	0.00	630.65
108	4-laning of Faraka-Raiganj	Road Transport & Highways	08/2013	1078.84	0.00	1108.40
109	4-laning of Brahampore-Faraka	Road Transport & Highways	08/2013	998.79	0.00	1034.80
110	Acquisition of Two nos. of 3060 DWT	Shipping & Ports	12/2011	277.03	280.00	294.87
111	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	Shipping & Ports	04/2009	245.67	298.17	371.18
112	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	Steel	10/2009	8692.00	0.00	9481.85
113	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREMENT EXP. UNIT	Steel	02/2011	230.00	0.00	246.84
