

**426th FLASH REPORT ON
CENTRAL SECTOR PROJECTS
(Rs.150 crore and above)
April, 2021**



KUDANKULAM NUCLEAR POWER PROJECT UNIT-3



सत्यमेव जयते

Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division

Khurshid Lal Bhawan, Janpath
New Delhi-110001
Website: www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India Ltd.
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead Travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised Catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Operation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petroleum Corporation Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative Ltd.
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation Ltd.
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Corporation.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Corporation.
NCL	Northern Coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation Ltd.
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corporation Ltd.
NGN	Next Generation Network
NLC	Neyveli Lignite Corporation Ltd.
NMDC	National Mineral Development Corporation Ltd.
NPC	Nuclear Power Corporation Ltd.
NRL	Numaligarh Refinery Ltd.
OB	Over Burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over Bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India Ltd.
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

EXECUTIVE SUMMARY


1. The Flash Report for April 2021 contains information on the status of the 1737 Central Sector Infrastructure Projects costing ₹150 crore and above.

2. During the reference month, 1737 projects, 525 projects are delayed with respect to their original schedules and 90 projects have reported additional delays vis-à-vis their date of completion reported in the previous month. Of these projects, 27 are Mega Projects costing ₹1000 crore and above. The sectorwise break up is tabulated below:

(All the figures are in number)

S. No.	Sector	Projects on monitor	Delayed Projects w.r.t original schedule	Additional delayed during the month under report	Additional delayed Mega Projects
1	ROAD TRANSPORT AND HIGHWAYS	908	118	18	4
2	RAILWAYS	312	148	8	5
3	PETROLEUM	139	78	21	8
4	COAL	101	52	10	1
5	POWER	78	43	15	5
6	WATER RESOURCES	49	13	0	0
7	URBAN DEVELOPMENT	33	9	1	0
8	HEALTH AND FAMILY WELFARE	29	10	0	0
9	HUMAN RESOURCE DEVELOPMENT	26	12	1	0
10	CIVIL AVIATION	19	14	4	1
11	STEEL	9	6	4	2
12	MINES	5	2	0	0
13	HOME AFFAIRS	5	2	0	0
14	ATOMIC ENERGY	4	4	0	0
15	FERTILISERS	4	4	2	0
16	RURAL DEVELOPMENT	4	3	3	0
17	TELECOMMUNICATIONS	3	3	1	1
18	FINANCE	2	1	1	0
19	DPIIT	2	2	0	0
20	HEAVY INDUSTRY	1	0	0	0
21	SHIPPING AND PORTS	1	0	0	0
22	DEFENCE PRODUCTION	1	1	1	0
23	COMMERCE	1	0	0	0
24	CULTURE DEVELOPMENT	1	0	0	0
Total		1737	525	90	27

3. Total original cost of implementation of the 1737 projects was ₹22,33,409.53 crore and their anticipated completion cost is likely to be ₹26,71,440.77 crore, which reflects overall cost overruns of ₹4,38,031.24 crore (19.61% of original cost). The expenditure incurred on these projects till April 2021 is ₹13,16,032.62 crore, which is 49.26% of the anticipated cost of the projects. The information can be viewed graphically as:

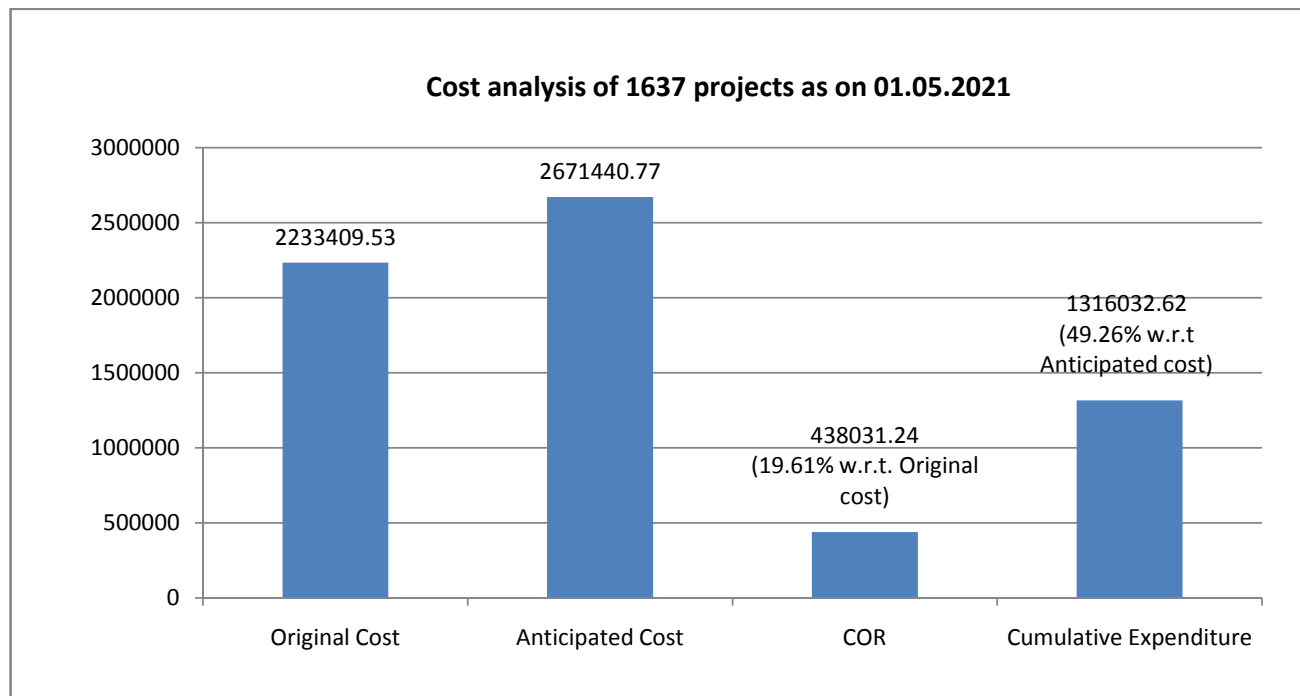


4. The sector-wise list of projects (maximum five in numbers) having maximum percentage of cost overruns and having maximum cost overruns in absolute term are at **Table A** and **Table B** respectively.

5. Out of the 1737 projects, 11 projects are ahead of schedule, 213 are on schedule, 525 are delayed, 470 projects reported cost overrun and 203 projects reported both time and cost overrun with respect to their original project implementation schedules. However, the number of delayed projects decreases to 375 if delay is calculated on the basis of latest schedule of completion. Further, for 988 projects neither the year of commissioning nor the tentative gestation period has been reported.


Status of projects (as on 01.05.2021)

(All the figures corresponds to number of project)

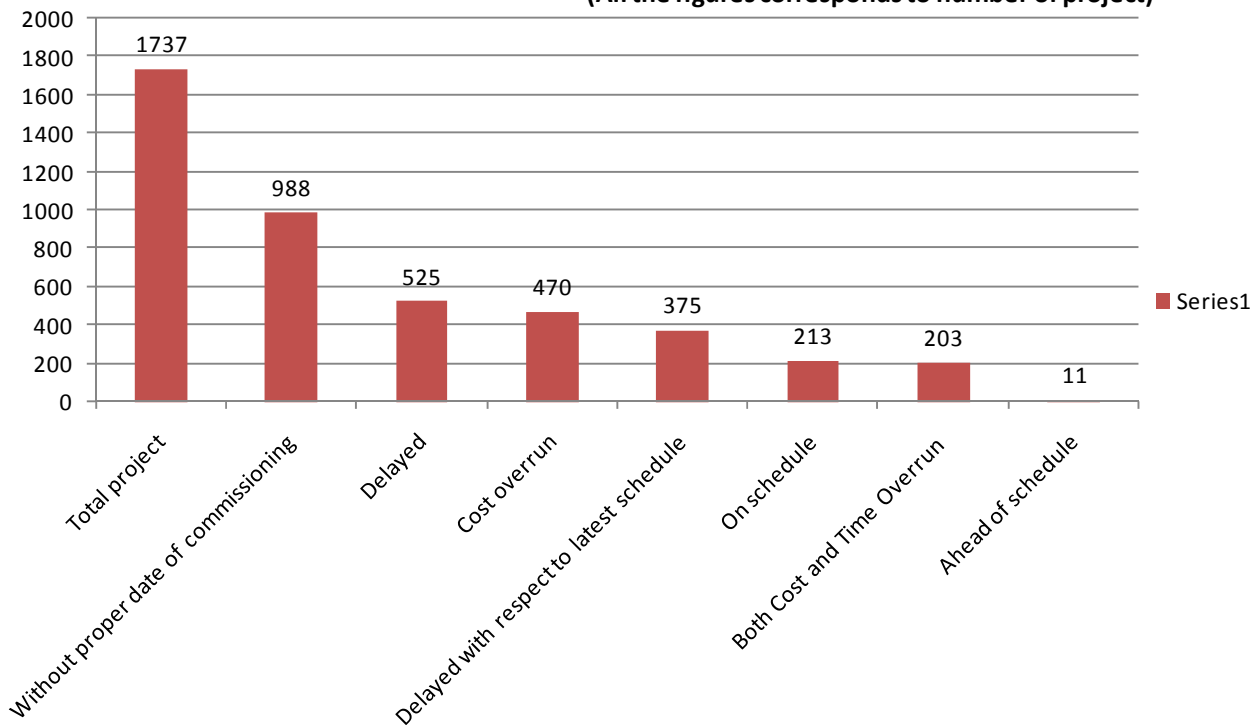


6. Out of 525 delayed projects, 106 (20%) projects have overall delay in the range of 1 to 12 months, 123 (23%) projects have delay in the range of 13 to 24 months, 179 (34%) projects have delay in the range of 25 to 60 months and 117 (22%) projects have delay of 61 months and above. The above information can be viewed graphically as shown below:

Break-up of 525 Delayed projects in April 2021

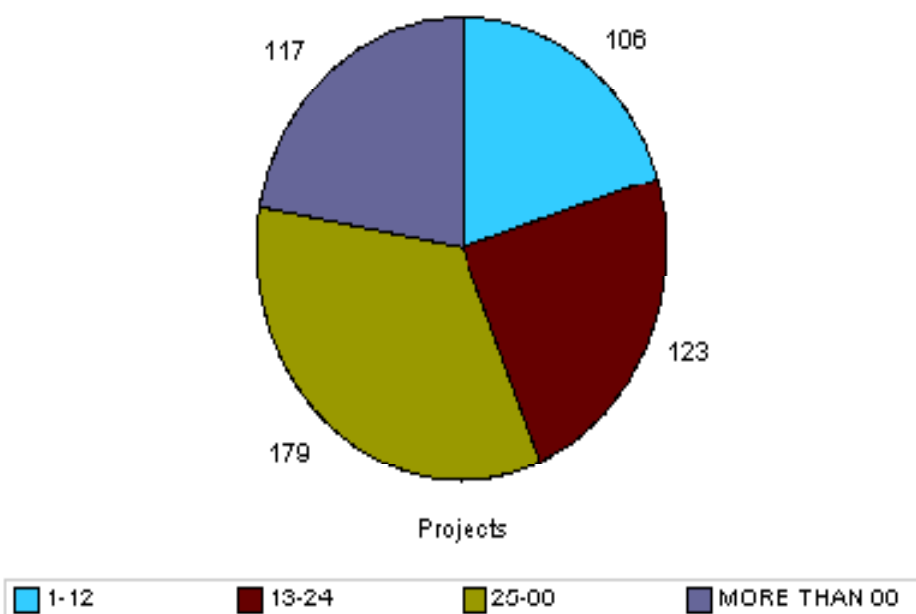

7. The status of online reporting of projects can be viewed month wise as:

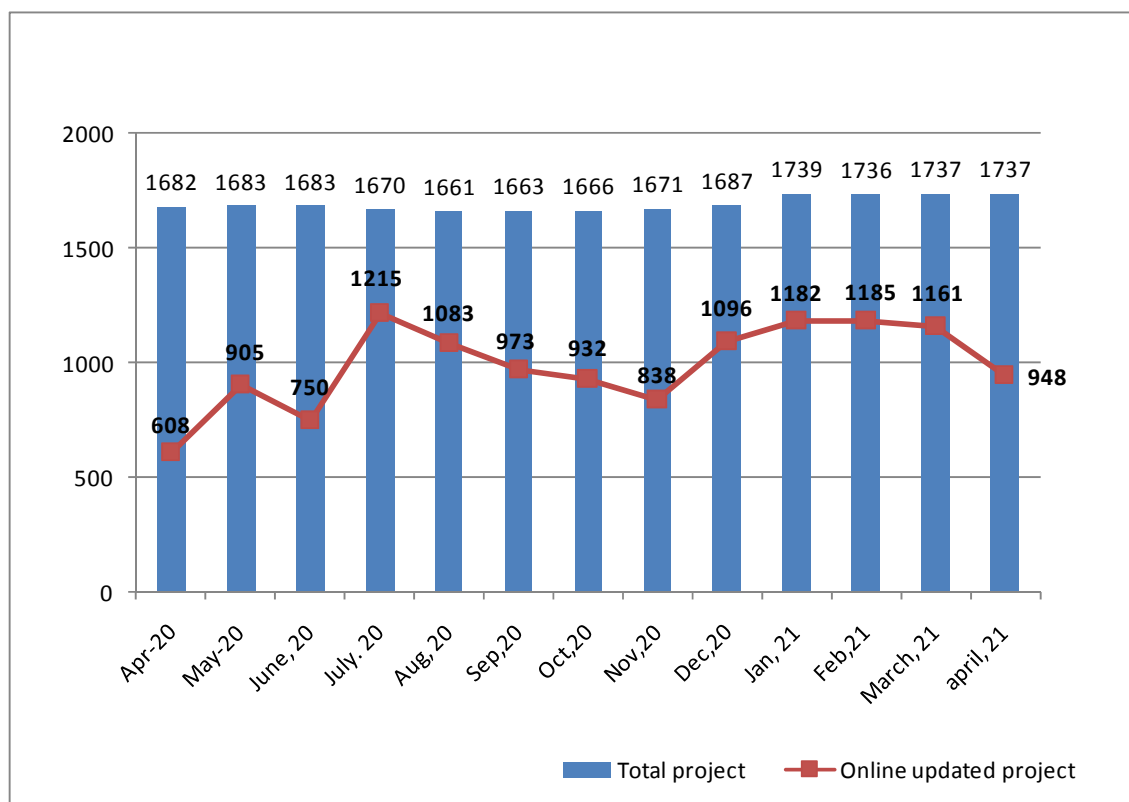

The average time overrun in these 525 delayed projects is 45.63 months. The sector wise list of projects (maximum five in numbers) having maximum time overruns (TOR) are at **Table-C**.

8. The brief reasons for time overruns as reported by various project implementing agencies are:

- Delay in land acquisition,
- Delay in obtaining forest/environment clearances,
- Lack of infrastructure support & linkages,
- Delay in tie-up of project financing,
- Delay in finalization of detailed engineering, change in scope,
- Delay in tendering,
- Delay in ordering & equipment supply,
- Law & order problems,
- Geological surprises,
- Pre-commissioning teething troubles and contractual issues.
- Contractual issues
- Inadequate manpower
- Delay in technical approval
- Encroachment
- State wise lockdown due to COVID 19

9. The Online Computerized Monitoring System (OCMS) of this Ministry envisages monitoring of milestones of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The sector wise list of earliest projects (maximum five in numbers) without milestones are at **Table-D**.

10. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The sector wise list of earliest (oldest) projects (maximum five in numbers) without revised cost estimates are at **Table-E**.

11. The sector wise list of earliest projects (maximum five in numbers) without revised commissioning schedule are at **Table-F**.

12. Based on the above information, the concerned administrative Ministry may like to review the projects in order to avoid further cost overrun, time overruns, to firm-up milestones in case of milestone is not available, to firm-up revised cost estimates and revised commissioning schedule if the same has been not revised and lapsed.

13. This has the approval of Competent Authority, Ministry of Statistics and Programme Implementation.

Table- A

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Percentage of Cost Overruns
(as on 01-05-2021)**

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (%)
	ATOMIC ENERGY				
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6840.00	95.88
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	16580.00	44.69
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12320.00	17079.00	38.63
	CIVIL AVIATION				
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	417.23	707.73	69.63
5	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	07/2018	346.27	480.33	38.72
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	1142.00	1232.00	7.88
	COAL				
7	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.49	201.44
8	BHATADI EXPANSION OC MINE	02/2016	304.52	729.86	139.68
9	BHANEAGAON OC	02/2015	187.94	409.68	117.98
10	RCE OF INDARAM OCP(1.20 MTPA)	07/2011	162.76	349.28	114.60
11	RANIGANJ MASTER PLAN	08/2009	2661.73	5146.48	93.35
	DPIIT				
12	DELHI MUMBAI INDUSTRIAL CORRIDOR	09/2011	12579.09	13812.30	9.80
13	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	4773.00	5178.00	8.49
	HEALTH AND FAMILY WELFARE				
14	AIIMS - MOTHER AND CHILD BLOCK	12/2013	204.44	250.00	22.29
15	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	156.56	190.34	21.58
16	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	499.23	20.55
17	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	07/2016	152.95	177.92	16.33
18	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR	03/2019	1577.00	1828.00	15.92
	HOME AFFAIRS				
19	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	2000.00	64.04
20	NSG AT KOLKATA	10/2014	162.88	238.00	46.12
	HUMAN RESOURCE DEVELOPMENT				
21	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	09/2013	484.32	626.26	29.31
22	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	08/2016	294.00	350.69	19.28
23	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P.	02/2019	186.00	205.00	10.22
24	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	12/2016	549.31	559.47	1.85
25	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	02/2016	496.18	498.99	0.57
	PETROLEUM				
26	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	2001.00	132.19
27	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	678.00	1472.00	117.11
28	LPG TERMINAL AT KOCHI	10/2015	607.06	1236.00	103.60
29	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	2915.00	5909.00	102.71
30	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	01/2015	1823.00	3027.90	66.09
	POWER				

31	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19992.43	218.08
32	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	7927.34	217.49
33	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	9897.59	152.52
34	BARH STPP(3X660MW) NTPC	02/2005	8692.97	21312.11	145.16
35	BRBCL-NABINAGAR TPP- JV (4X250 MW)	01/2007	5353.00	10566.00	97.38
RAILWAYS					
36	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	8248.50	3230.57
37	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI	04/2011	120.70	2172.16	1699.64
38	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	27949.00	1017.96
39	BIHTA-AURANGABAD (NL)	04/2008	326.20	2995.01	818.15
40	RAMGANJMUNDI-BHOPAL (NL),WCR	04/2001	424.60	2909.99	585.35
ROAD TRANSPORT AND HIGHWAYS					
41	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM	12/2017	217.96	884.00	305.58
42	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	655.17	234.27
43	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2967.50	167.82
44	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	167.64	435.78	159.95
45	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	04/2013	151.59	370.01	144.09
RURAL DEVELOPMENT					
46	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	155.66	3.96
47	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	202.61	207.12	2.23
STEEL					
48	NMDC INTEGRATED STEEL PLANT	01/2010	15525.00	21940.00	41.32
TELECOMMUNICATIONS					
49	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	84.97
URBAN DEVELOPMENT					
50	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	114.26	266.00	132.80
51	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	23136.00	33406.00	44.39
52	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	19058.00	30.53
53	KOCHI METRO RAIL PROJECT	07/2012	5181.79	6218.14	20.00
54	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	10773.00	12787.00	18.69
WATER RESOURCES					
55	POLAVARAM IRRIGATION PROJECT	02/2009	10151.04	55548.87	447.22
56	FARRUKHABAD I AND D AND STP WORKS HAM	10/2017	213.62	261.12	22.24
57	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA	02/2011	279.91	330.05	17.91
58	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR	10/2016	370.40	430.49	16.22
59	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA	05/2018	198.43	224.69	13.23

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overrun.

Table - B

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Cost Overruns (COR)
(as on 01-05-2021)**

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (Rs.crore)
7					

	ATOMIC ENERGY				
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	16580.00	5121.00
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12320.00	17079.00	4759.00
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6840.00	3348.00
	CIVIL AVIATION				
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	417.23	707.73	290.50
5	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	07/2018	346.27	480.33	134.06
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	1142.00	1232.00	90.00
	COAL				
7	RANIGANJ MASTER PLAN	08/2009	2661.73	5146.48	2484.75
8	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	06/2011	5907.11	7980.79	2073.68
9	BHATADI EXPANSION OC MINE	02/2016	304.52	729.86	425.34
10	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.49	307.06
11	BHANEGAON OC	02/2015	187.94	409.68	221.74
	DPIIT				
12	DELHI MUMBAI INDUSTRIAL CORRIDOR	09/2011	12579.09	13812.30	1233.21
13	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	4773.00	5178.00	405.00
	HEALTH AND FAMILY WELFARE				
14	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR	03/2019	1577.00	1828.00	251.00
15	AIIMS BILASPUR	04/2018	1351.00	1471.00	120.00
16	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	499.23	85.12
17	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	585.00	79.42
18	AIIMS - MOTHER AND CHILD BLOCK	12/2013	204.44	250.00	45.56
	HOME AFFAIRS				
19	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	2000.00	780.79
20	NSG AT KOLKATA	10/2014	162.88	238.00	75.12
	HUMAN RESOURCE DEVELOPMENT				
21	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	09/2013	484.32	626.26	141.94
22	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	08/2016	294.00	350.69	56.69
23	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P.	02/2019	186.00	205.00	19.00
24	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	12/2016	549.31	559.47	10.16
25	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	02/2016	496.18	498.99	2.81
	PETROLEUM				
26	VISAKH REFINERY MODERNISATION PROJECT	07/2016	20928.00	26264.00	5336.00
27	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	2915.00	5909.00	2994.00
28	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	05/2016	4497.00	6025.00	1528.00
29	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	01/2015	1823.00	3027.90	1204.90
30	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	2001.00	1139.21
	POWER				
31	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19992.43	13707.10
32	BARH STPP(3X660MW) NTPC	02/2005	8692.97	21312.11	12619.14
33	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	9897.59	5978.00
34	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	7927.34	5430.44
35	BRBCL-NABINAGAR TPP- JV (4X250 MW)	01/2007	5353.00	10566.00	5213.00
	RAILWAYS				
36	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	16592.00	51101.00	34509.00

37	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	27949.00	25449.00
38	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	11589.00	28181.00	16592.00
39	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	8248.50	8000.84
40	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	4454.17	12264.15	7809.98
ROAD TRANSPORT AND HIGHWAYS					
41	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2967.50	1859.50
42	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	03/2016	1587.49	2982.00	1394.51
43	DELHI AGRA APPROVED LENGTH 180.0 KM	10/2012	1928.22	3182.34	1254.12
44	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	08/2016	1388.34	2587.50	1199.16
45	4 LANING FROM PHAGWARA TO RUPNAGAR	08/2016	1169.61	2280.00	1110.39
RURAL DEVELOPMENT					
46	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	155.66	5.93
47	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	202.61	207.12	4.51
STEEL					
48	NMDC INTEGRATED STEEL PLANT	01/2010	15525.00	21940.00	6415.00
TELECOMMUNICATIONS					
49	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	11330.00
URBAN DEVELOPMENT					
50	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	23136.00	33406.00	10270.00
51	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	19058.00	4458.00
52	BANGALORE METRO RAIL PROJECT PHASE-2	02/2014	26405.14	30695.12	4289.98
53	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	10773.00	12787.00	2014.00
54	KOCHI METRO RAIL PROJECT	07/2012	5181.79	6218.14	1036.35
WATER RESOURCES					
55	POLAVARAM IRRIGATION PROJECT	02/2009	10151.04	55548.87	45397.83
56	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR	10/2016	370.40	430.49	60.09
57	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA	02/2011	279.91	330.05	50.14
58	FARRUKHABAD I AND D AND STP WORKS HAM	10/2017	213.62	261.12	47.50
59	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA	05/2018	198.43	224.69	26.26

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overruns.

Table -C

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Time Overruns (TOR)
(as on 01-05-2021)**

SN	PROJECT	DOA	DOC ORIGINAL	DOC ANTICIPATED	TOR (IN MONTHS)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	09/2010	10/2022	145
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016	03/2023	75
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	02/2022	74
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	03/2013	11/2020	11/2023	36
CIVIL AVIATION					
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	09/2018	06/2021	33
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	09/2015	06/2019	06/2021	24
7	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	11/2016	04/2020	03/2022	23
8	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT	08/2017	02/2020	12/2021	22
9	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	01/2016	03/2020	12/2021	21
COAL					
10	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY)	12/2007	03/2010	03/2029	228
11	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY)	12/2007	03/2013	03/2028	180
12	BHUBANESWARI EXPENSION OCP(40.0 MTY)	12/2007	03/2017	03/2031	168
13	MAGADH EXPANSION OC(51 MTY)	08/2008	07/2012	03/2025	152
14	CHURI BENTI UG (0.81 MTY)	08/2007	03/2011	03/2022	132
DEFENCE PRODUCTION					
15	RESIDENTIAL QUATERS FOR HAL,BANGLORE	12/2016	02/2020	12/2021	22
DPIIT					
16	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	12/2019	12/2021	24
17	DELHI MUMBAI INDUSTRIAL CORRIDOR	09/2011	09/2019	07/2021	22
FERTILISERS					
18	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT	01/2018	11/2019	05/2021	18
19	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA	01/2018	11/2019	04/2021	17
20	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL	01/2018	11/2019	04/2021	17
21	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY	04/2018	04/2020	07/2021	15
FINANCE					
22	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	12/2015	10/2019	07/2021	21
HEALTH AND FAMILY WELFARE					
23	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	11/2013	05/2021	90
24	NEIGRIHMS SHILLONG MEGHALYA	10/2016	05/2018	12/2021	43
25	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	08/2017	03/2019	06/2021	27
26	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST	09/2017	03/2020	12/2021	21
27	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT	03/2018	09/2020	04/2022	19
HOME AFFAIRS					
28	NSG AT KOLKATA	10/2014	04/2018	12/2021	44

29	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	10/2019	12/2021	26
	HUMAN RESOURCE DEVELOPMENT				
30	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	09/2012	03/2016	06/2021	63
31	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	02/2016	06/2017	10/2021	52
32	PERMANENT CAMPUS FOR IIM BODH GAYA	09/2018	09/2020	11/2022	26
33	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	08/2016	04/2019	05/2021	25
34	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	01/2018	05/2020	02/2022	21
	MINES				
35	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN	11/2017	04/2021	03/2023	23
36	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/2014	04/2021	12/2022	20
	PETROLEUM				
37	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	12/2012	02/2022	110
38	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	05/2013	02/2022	105
39	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	02/2017	08/2022	66
40	LPG TERMINAL AT KOCHI	10/2015	10/2017	03/2022	53
41	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	12/2015	04/2018	05/2022	49
	POWER				
42	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	09/2010	08/2023	155
43	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	09/2009	07/2022	154
44	BARH STPP(3X660MW) NTPC	02/2005	10/2011	07/2023	141
45	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	08/2008	06/2013	12/2023	126
46	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	03/2013	12/2022	117
	RAILWAYS				
47	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	04/1998	03/2003	03/2030	324
48	MUNEERABAD-MAHABOBNAGAR(NL),SCR	04/1997	03/2000	03/2023	276
49	BANGLORE - SATYAMANGALAM (NL)(SWR)	04/1996	03/2002	03/2024	264
50	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	11/2002	12/2022	241
51	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL	04/2010	03/2005	03/2025	240
	ROAD TRANSPORT AND HIGHWAYS				
52	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	08/2010	10/2010	06/2021	128
53	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	08/2010	10/2010	06/2021	128
54	4-LANING OF BRAHAMPORE-FARAKA	02/2011	08/2013	06/2022	106
55	VARANASI-AURANGABAD KM.786 TO KM.978.40	09/2011	03/2014	12/2022	105
56	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	01/2013	02/2013	06/2021	100
	RURAL DEVELOPMENT				
57	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	12/2015	10/2021	70
58	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	12/2016	12/2021	60
59	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016	10/2021	58
	STEEL				
60	NMDC INTEGRATED STEEL PLANT	10/2010	05/2015	07/2021	74

61	NEW SINTER PLANT AT BOKARO STEEL PLANT	03/2015	10/2017	12/2021	50
62	COKE OVEN BATTERY-5	12/2011	12/2017	12/2021	48
63	FORGED WHEEL PLANT	04/2014	09/2018	06/2021	33
64	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	11/2016	06/2019	08/2021	26
TELECOMMUNICATIONS					
65	NETWORK FOR SPECTRUM	03/2012	07/2015	07/2021	72
66	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	10/2016	03/2018	06/2021	39
67	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART	03/2020	06/2021	11/2021	5
URBAN DEVELOPMENT					
68	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	01/2015	03/2023	98
69	DELHI MRTS PHASE-III	09/2011	03/2016	09/2021	66
70	BANGALORE METRO RAIL PROJECT PHASE-2	02/2014	02/2019	06/2024	64
71	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	12/2018	08/2022	44
72	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I	10/2016	07/2021	12/2024	41
WATER RESOURCES					
73	POLAVARAM IRRIGATION PROJECT	02/2009	03/2020	04/2022	25
74	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA	03/2017	12/2019	12/2021	24
75	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR	02/2014	12/2019	05/2021	17
76	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR	04/2015	04/2020	06/2021	14
77	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2	05/2016	12/2021	12/2022	12

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further time overruns.

Table – D

**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Milestones
(as on 01-05-2021)**

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST ANTICIPATED (Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)	ORIGINAL DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
CIVIL AVIATION							
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	09/2015	438.28	438.28	335.58	06/2019	N.A.
2	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA	01/2016	458.00	458.00	135.60	03/2020	12/2021
3	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPORT	11/2016	303.80	303.80	115.88	04/2020	05/2021
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	1142.00	1232.00	323.90	03/2021	03/2022
5	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT	01/2018	1405.00	1405.00	199.55	08/2022	08/2022
COAL							
6	BARSINGSAR THERMAL POWER STATION EXTENSION	03/2015	2112.60	2112.60	86.85	09/2020	N.A.
7	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	03/2015	513.63	513.63	175.30	12/2019	N.A.
8	BITHNOK LIGNITE THERMAL POWER STATION	03/2015	2196.30	2196.30	140.80	09/2020	N.A.
9	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	03/2015	522.45	522.45	9.88	09/2019	N.A.
10	PATHERDIH 2.5 NLW COAL WASHERY	10/2015	243.00	334.27	18.35	04/2018	06/2022
COMMERCE							
11	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI	06/2018	302.64	302.64	60.00	10/2020	N.A.
DPIIT							
12	DELHI MUMBAI INDUSTRIAL CORRIDOR	09/2011	12579.09	13812.30	8715.07	09/2019	07/2021
13	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	4773.00	5178.00	2432.15	12/2019	12/2021
HEALTH AND FAMILY WELFARE							
14	LGBRIMH-TEZPUR, ASSAM	07/2012	175.57	175.57	163.37	12/2014	03/2018
15	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	499.23	488.22	11/2013	05/2021
16	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	07/2016	703.00	557.48	469.13	06/2020	07/2021
17	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	07/2016	785.00	715.06	548.39	04/2020	07/2021
18	CNCI KOLKATA WEST BENGAL	08/2016	244.00	248.00 ³	224.92	09/2018	05/2019

HEAVY INDUSTRY							
19	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	08/2016	1554.00	900.00	815.00	09/2019	N.A.
HOME AFFAIRS							
20	BUILDING OF THE FORCE HEADQUARTER INCLUDING SECTOR HQR RAF	06/2019	277.35	277.35	5.30	07/2022	07/2022
21	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE-	01/2020	166.98	166.98	0.00	10/2023	10/2023
22	CONSTRUCTION OF SEPARATE FAMILY ACCOMMODATION (440 NOS.) (PHASE- C/O 336 NOS. TYPE- II QTRS . 96	01/2020	166.98	166.98	0.29	05/2022	05/2022
HUMAN RESOURCE DEVELOPMENT							
23	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	09/2013	484.32	626.26	0.00	09/2014	N.A.
24	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR	11/2017	171.72	171.72	53.94	03/2020	06/2021
25	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C)	01/2018	676.00	676.00	0.00	04/2023	04/2023
26	STUDY IN INDIA	03/2018	150.00	150.00	0.00	04/2018	N.A.
27	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION	08/2018	418.00	418.00	110.00	03/2019	N.A.
PETROLEUM							
28	IRUGUR- DEVANGONTHI POL PIPELINE	11/2012	678.00	1472.00	18.80	02/2017	08/2022
29	ENNORE-TRICHY- MADURAI LPG PIPELINE	05/2013	711.00	711.00	11.12	06/2020	N.A.
30	KOCHI SALEM LPG PIPELINE PROJECT	12/2015	1112.00	1507.24	725.00	06/2019	02/2022
31	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI- MANMAD- AHMEDNAGAR- SOLAPUR PIPELI	05/2016	261.00	261.00	157.94	01/2021	04/2021
32	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI- MANMAD- AHMEDNAGAR- SOLAPUR PIPELINE	05/2016	212.00	212.00	146.57	01/2021	04/2021
POWER							
33	LOKTAK D/S HEP(NHPC)	12/1999	578.62	578.62	0.00	06/2006	N.A.
34	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19992.43	13537.76	09/2010	08/2023
35	PAKRI BARWADIH COAL MINING	10/2004	4237.96	4552.00	3380.97	10/2017	N.A.

	PROJECT						
36	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	01/2014	374.63	374.63	241.68	04/2016	06/2021
37	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	10/2014	8112.12	8112.12	1706.23	04/2020	07/2025
RAILWAYS							
38	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	393.46	1026.00	182.49	03/2007	N.A.
39	NANGALDAM-TALWARA(NL),NR	03/1981	450.00	2200.00	714.78	07/2012	03/2024
40	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	297.32	614.00	275.06	03/2019	N.A.
41	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	04/1987	406.99	545.70	149.30	03/2006	03/2025
42	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	332.15	546.71	541.83	07/2014	N.A.
ROAD TRANSPORT AND HIGHWAYS							
43	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	01/1991	478.35	478.35	446.62	N.A.	N.A.
44	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	01/1991	319.68	369.77	238.01	N.A.	N.A.
45	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	01/1991	219.40	219.40	0.00	01/2018	N.A.
46	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	282.41	322.01	318.64	08/2016	N.A.
47	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	358.22	377.64	343.70	10/2016	N.A.
SHIPPING AND PORTS							
48	JAL MARG VIKAS PROJECT	01/2018	5369.18	4633.81	1814.28	03/2023	03/2023
STEEL							
49	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP	11/2020	542.24	542.24	31.60	12/2023	12/2023
50	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY	11/2020	377.18	377.18	16.12	05/2023	05/2023
TELECOMMUNICATIONS							

51	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	16594.00	07/2015	06/2021
52	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	10/2016	248.20	248.20	133.09	03/2018	06/2021
53	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART	03/2020	431.16	431.16	0.00	06/2021	11/2021
URBAN DEVELOPMENT							
54	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	114.26	266.00	0.00	12/2013	N.A.
55	DELHI MRTS PHASE-III	09/2011	38585.00	38585.00	39838.90	03/2016	09/2021
56	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	07/2012	884.30	884.30	812.00	12/2015	N.A.
57	KOCHI METRO RAIL PROJECT	07/2012	5181.79	6218.14	6059.17	07/2017	09/2020
58	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	23136.00	33406.00	17039.36	01/2015	03/2023
WATER RESOURCES							
59	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA	02/2011	279.91	330.05	222.79	12/2019	01/2021
60	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR	02/2014	274.76	274.76	201.30	12/2019	05/2021
61	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	225.77	225.77	271.22	03/2020	03/2021
62	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE	12/2014	272.32	272.32	214.52	04/2020	03/2021
63	SAIDPUR SEWER NETWORK PATNA	04/2015	268.63	268.63	286.36	01/2021	N.A.

N.A.: Not Available.

Table-E

**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Cost Estimates
(as on 01-05-2021)**

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST REVISED(Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	5677.00	5922.21
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	0.00	16488.00
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	10/2009	12320.00	0.00	13158.00
COAL					
4	RCE OF INDARAM OCP(1.20 MTPA)	07/2011	162.76	0.00	288.72
5	AMALGAMATED GONDEGAON GHATROHAN OC	02/2016	198.68	0.00	246.55
HEALTH AND FAMILY WELFARE					
6	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	0.00	488.22
7	AIIMS - MOTHER AND CHILD BLOCK	12/2013	204.44	0.00	233.39
8	AIIMS - OPD(NEW)	08/2014	293.65	0.00	299.76
9	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	0.00	586.96
10	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	168.90	0.00	169.51
PETROLEUM					
11	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	07/2011	352.56	0.00	455.00
12	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	11/2014	4588.29	0.00	4977.00
13	PARADIP HYDERABAD PIPELINE	01/2015	2321.00	0.00	2888.48
14	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	01/2015	1823.00	0.00	1933.53
POWER					
15	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	7927.34	8154.50
16	SYSTEM STRENGTHENING XIII OF SR GRID	10/2011	487.49	0.00	590.30
17	MUNPL-MEJA TPP - JV (2X660 MW)	04/2012	9750.89	0.00	11130.00
18	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	12/2012	11846.00	0.00	13766.78
19	KHARGONE STPP STAGE I (1320 MW)	03/2015	9870.51	0.00	10019.31
RAILWAYS					
20	NANGALDAM-TALWARA(NL),NR	03/1981	450.00	0.00	714.78
21	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	332.15	0.00	541.83
22	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	04/1991	329.39	0.00	1207.34
23	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	0.00	23132.28
24	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	09/1995	303.98	0.00	697.29
ROAD TRANSPORT AND HIGHWAYS					
25	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	282.41	0.00	318.64
26	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	280.00	0.00	612.58
27	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	0.00	325.28
28	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	155.04	0.00	251.39
29	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	0.00	655.17
TELECOMMUNICATIONS					
30	NETWORK FOR SPECTRUM	03/2012	13334.00	0.00	16594.00
URBAN DEVELOPMENT					
31	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	0.00	16365.87
32	DELHI MRTS PHASE-III	09/2011	38585.00	0.00	39838.90
33	REDEVELOPMENT OF EAST KIDWAI NAGAR	06/2012	4264.00	0.00	4683.08
WATER RESOURCES					

34	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	225.77	0.00	271.22
35	SAIDPUR SEWER NETWORK PATNA	04/2015	268.63	0.00	286.36

N.B.: The concerned administrative Ministry may like to review these Projects in order to firm-up revised cost estimates.

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Commissioning Schedule (as on 01-05-2021)

SN	SECTOR/ PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	REVISED DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
	CIVIL AVIATION				
SN	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	09/2015	06/2019	N.A.	N.A.
	COAL				
1	RANIGANJ MASTER PLAN	08/2009	08/2019	N.A.	N.A.
2	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	06/2011	12/2015	N.A.	02/2021
3	PATHERDIH NLW WASHERY	10/2012	04/2014	N.A.	04/2020
4	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	03/2015	09/2019	N.A.	N.A.
5	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	03/2015	12/2019	N.A.	N.A.
	COMMERCE				
6	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI	06/2018	10/2020	N.A.	N.A.
	HEALTH AND FAMILY WELFARE				
7	LGBRIMH-TEZPUR, ASSAM	07/2012	12/2014	N.A.	03/2018
8	AIIMS - OPD(NEW)	08/2014	05/2017	N.A.	01/2020
9	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	03/2018	N.A.	09/2019
10	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	05/2017	N.A.	07/2019
11	CNCI KOLKATA WEST BENGAL	08/2016	09/2018	N.A.	05/2019
	HEAVY INDUSTRY				
12	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	08/2016	09/2019	N.A.	N.A.
	HUMAN RESOURCE DEVELOPMENT				
13	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	10/2012	N.A.	N.A.
14	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	11/2012	11/2014	N.A.	N.A.
15	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	09/2013	09/2014	N.A.	N.A.
16	STUDY IN INDIA	03/2018	04/2018	N.A.	N.A.
17	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION	08/2018	03/2019	N.A.	N.A.
	MINES				
18	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	12/2015	11/2020	N.A.	02/2021
19	UTKAL D AND E COAL BLOCK	05/2016	01/2020	N.A.	N.A.
	PETROLEUM				
20	ENNORE-TRICHY-MADURAI LPG PIPELINE	05/2013	06/2020	N.A.	N.A.
21	MUMBAI REFINERY EXPANSION PROJECT	09/2015	03/2020	N.A.	N.A.
22	BS-VI PROJECTS	09/2017	12/2019	N.A.	01/2021
	POWER				
23	LOKTAK D/S HEP(NHPC)	12/1999	06/2006	N.A.	N.A.
24	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017	N.A.	N.A.
25	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009	02/2021	02/2021
26	SYTEM STRENGTHENING XIII OF SR GRID	10/2011	06/2014	N.A.	N.A.
27	MOUDA STPP STAGE 2	03/2012	09/2016	N.A.	N.A.
	RAILWAYS				
28	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	03/2007	03/2007	N.A.
29	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983 ¹⁹	03/2019	N.A.	N.A.

30	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	07/2014	N.A.	N.A.
31	NANDYAL-YERRAGUNTALA(NL),SCR	03/1996	02/2009	N.A.	N.A.
32	HARIDASPUR-PARADEEP(NL)	04/1996	12/2017	N.A.	N.A.
ROAD TRANSPORT AND HIGHWAYS					
33	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O	01/1991	04/2014	N.A.	N.A.
34	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	08/2016	N.A.	N.A.
35	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	10/2016	N.A.	N.A.
36	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB	01/1991	10/2017	N.A.	N.A.
37	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	01/1991	01/2018	N.A.	N.A.
STEEL					
38	COKE OVEN BATTERY-5	12/2011	12/2017	12/2020	12/2020
URBAN DEVELOPMENT					
39	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	12/2013	N.A.	N.A.
40	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	12/2015	N.A.	N.A.
41	REDEVELOPMENT OF EAST KIDWAI NAGAR	06/2012	11/2019	N.A.	N.A.
42	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	07/2012	12/2015	N.A.	N.A.
43	KOCHI METRO RAIL PROJECT	07/2012	07/2017	09/2020	09/2020
WATER RESOURCES					
44	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA	02/2011	12/2019	N.A.	01/2021
45	SAIDPUR SEWER NETWORK PATNA	04/2015	01/2021	N.A.	N.A.
46	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI	03/2017	08/2019	N.A.	N.A.
47	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO	05/2017	05/2020	N.A.	N.A.
48	I AND D AND STP WORKS FOR BHAGALPUR	10/2017	09/2020	N.A.	N.A.

N.A.: Not Available.

TABLE-1

EXECUTIVE SUMMARY COSTING Rs. 150 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	908	18
2	RAILWAYS	312	8
3	PETROLEUM	139	21
4	COAL	101	10
5	POWER	78	15
6	WATER RESOURCES	49	0
7	URBAN DEVELOPMENT	33	1
8	HEALTH AND FAMILY WELFARE	29	0
9	HUMAN RESOURCE DEVELOPMENT	26	1
10	CIVIL AVIATION	19	4
11	STEEL	9	4
12	MINES	5	0
13	HOME AFFAIRS	5	0
14	ATOMIC ENERGY	4	0
15	FERTILISERS	4	2
16	RURAL DEVELOPMENT	4	3
17	TELECOMMUNICATIONS	3	1
18	FINANCE	2	1
19	DPIIT	2	0
20	HEAVY INDUSTRY	1	0
21	SHIPPING AND PORTS	1	0
22	DEFENCE PRODUCTION	1	1
23	COMMERCE	1	0
24	CULTURE DEVELOPMENT	1	0
	Total	1737	90

TABLE-2

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2021-2022				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)

TABLE-3

Month wise List of Deleted Projects Costing Rs. 150 crore and above during				
2021-2022				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)

TABLE-4

Projects Added / Completed / Dropped / Frozen Rs. 150 Crore and above

No of Projects in Previous Month	1737
No of Projects Completed/Dropped/Frozen in Current Month	0
No of Projects added in Current Month	0
No of Projects in Current Month	1737

Project status Rs. 150 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	525 (30.22%)	11 (.63%)	213 (12.26%)	106 (6.10%)	882 (50.78%)	1737
Latest Approved (Date)	375 (21.59%)	23 (1.32%)	361 (20.78%)	96 (5.53%)	882 (50.78%)	1737

Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	1471	18,05,955.02	20,28,284.73	9,49,633.43	46.80	2,22,329.71	12.30
Project with Revision in Cost	266	6,39,362.44	6,43,156.04	3,66,399.19	57.00	3,793.60	.60
Total	1,737	24,45,317.46	26,71,440.77	13,16,032.62	49.26	2,26,123.31	9.25
Original Cost of All Projects							
Original Cost	1,737	22,33,409.53	26,71,440.77	13,16,032.62	49.26	4,38,031.24	19.61

Delayed Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	525	9,15,431.94	11,97,201.16	6,87,640.77	57.40	2,81,769.22	30.78
Latest Approved (RCE)	375	6,83,290.33	8,28,116.80	4,59,908.57	55.50	1,44,826.47	21.20

Additional Delayed Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Latest Approved	90	1,03,082.39	1,29,657.06	93,751.63	72.30	26,574.67	25.80
Total	90	1,03,082.39	1,29,657.06	93,751.63	72.31	26,574.67	25.78

TABLE-5

Extent of cost overrun in projects with respect to original cost (Sector Wise)						Rs. 150 Crore and above			
						(All Cost/ Expenditure in Rs. crore)			
						Projects with cost overrun [^]			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	48.51
2	CIVIL AVIATION	19	13,786.34	14,264.62	3.47	3	1,905.50	2,420.06	27.00
3	COAL	101	1,45,653.01	1,44,995.00	-0.45	20	31,389.63	37,889.80	20.71
4	FINANCE	2	557.77	557.73	-0.01	0	0.00	0.00	0.00
5	FERTILISERS	4	1,101.28	1,101.28	0.00	0	0.00	0.00	0.00
6	MINES	5	7,078.62	7,075.17	-0.05	0	0.00	0.00	0.00
7	STEEL	9	25,452.51	31,567.51	24.03	1	15,525.00	21,940.00	41.32
8	PETROLEUM	139	2,96,976.45	3,04,256.68	2.45	27	62,139.58	81,216.86	30.70
9	POWER	78	2,95,137.42	3,67,699.63	24.59	32	1,75,198.45	2,49,834.01	42.60
10	HEAVY INDUSTRY	1	1,554.00	900.00	-42.08	0	0.00	0.00	0.00
11	HEALTH AND FAMILY WELFARE	29	15,273.26	15,628.51	2.33	12	5,589.39	6,287.30	12.49
12	RAILWAYS	312	4,62,095.03	7,00,076.37	51.50	211	2,29,432.02	4,78,447.32	108.54
13	ROAD TRANSPORT AND HIGHWAYS	908	5,40,947.36	5,61,176.00	3.74	135	94,703.35	1,21,666.27	28.47
14	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0.00
15	TELECOMMUNICATIONS	3	14,013.36	25,343.36	80.85	1	13,334.00	24,664.00	84.97
16	URBAN DEVELOPMENT	33	2,82,500.28	3,05,097.88	8.00	7	84,474.19	1,07,150.99	26.84
17	WATER RESOURCES	49	26,781.06	72,049.94	169.03	7	12,126.97	57,719.96	375.96
18	DEFENCE PRODUCTION	1	246.31	210.00	-14.74	0	0.00	0.00	0.00
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	0.00
20	HUMAN RESOURCE DEVELOPMENT	26	11,077.40	11,265.83	1.70	5	2,009.81	2,240.41	11.47
21	HOME AFFAIRS	5	1,993.40	2,849.31	42.94	2	1,382.09	2,238.00	61.93

Extent of cost overrun in projects with respect to original cost (Sector Wise)						Rs. 150 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
22	RURAL DEVELOPMENT	4	889.43	899.87	1.17	2	352.34	362.78	2.96
23	CULTURE DEVELOPMENT	1	151.33	151.33	0.00	0	0.00	0.00	0.00
24	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	9.44
Total		1737	22,33,409.53	26,71,440.77	19.61	470	7,74,185.41	12,53,567.06	61.92

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-6

Extent of cost overrun in projects with respect to original cost (State Wise) Rs.							150	Crore and above	
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun^			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	77	1,22,880.98	1,70,411.65	38.68	16	47,279.32	1,04,034.99	120.04
2	ARUNACHAL PRADESH	42	24,624.65	44,366.68	80.17	10	12,055.29	31,797.32	163.76
3	ASSAM	47	42,046.33	45,563.88	8.37	19	9,301.62	14,229.97	52.98
4	BIHAR	108	1,22,099.62	1,58,462.50	29.78	35	42,074.64	79,557.34	89.09
5	GOA	11	5,629.77	5,640.26	0.19	2	529.17	539.66	1.98
6	GUJARAT	59	1,06,069.60	1,17,304.95	10.59	17	33,456.55	45,670.99	36.51
7	HARYANA	43	30,316.35	32,837.14	8.32	7	3,872.20	6,803.47	75.70
8	HIMACHAL PRADESH	15	20,365.24	30,249.67	48.54	3	8,237.58	18,122.01	119.99
9	JAMMU AND KASHMIR	22	40,412.13	66,473.44	64.49	4	6,582.27	32,776.33	397.95
10	KARNATAKA	60	71,320.53	80,896.72	13.43	15	43,150.08	53,060.00	22.97
11	KERALA	22	37,466.85	42,584.93	13.66	12	18,147.21	23,289.33	28.34
12	MADHYA PRADESH	84	91,161.40	1,04,808.86	14.97	20	35,307.11	49,952.02	41.48
13	MAHARASHTRA	242	2,17,334.38	2,41,218.69	10.99	37	63,879.11	93,039.91	45.65
14	MANIPUR	12	8,137.49	15,887.67	95.24	1	4,454.17	12,264.15	175.34
15	MEGHALAYA	7	3,245.09	6,563.59	102.26	2	1,390.78	4,709.28	238.61
16	MIZORAM	18	9,030.03	12,978.73	43.73	5	3,593.57	7,542.27	109.88
17	NAGALAND	38	18,265.97	22,463.91	22.98	2	2,699.59	7,298.00	170.34
18	ODISHA	89	1,29,891.78	1,34,147.04	3.28	17	27,755.43	36,328.65	30.89
19	PUNJAB	29	15,325.05	18,249.98	19.09	8	5,301.19	8,645.53	63.09
20	RAJASTHAN	60	53,090.50	61,137.54	15.16	14	19,890.78	27,938.05	40.46
21	SIKKIM	14	5,074.99	12,994.31	156.05	5	2,227.62	10,146.94	355.51
22	TAMIL NADU	71	1,19,185.26	1,38,369.59	16.10	23	39,340.59	60,197.60	53.02
23	TRIPURA	13	3,479.87	3,626.40	4.21	3	921.97	1,104.78	19.83
24	UTTAR PRADESH	134	1,78,012.58	1,85,467.12	4.19	33	56,372.60	66,070.83	17.20
25	WEST BENGAL	75	65,583.67	84,487.51	28.82	29	29,934.59	49,180.29	64.29
26	A & N ISLANDS	9	2,888.63	3,159.99	9.39	2	655.03	945.73	44.38
27	CHANDIGARH	2	349.15	570.00	63.25	2	349.15	570.00	63.25
28	DELHI	36	90,723.12	92,153.92	1.58	9	11,777.30	13,941.30	18.37
29	PONDICHERRY	1	195.00	195.00	0.00	0	0.00	0.00	0.00
30	CHHATISGARH	48	91,239.04	1,02,416.44	12.25	12	39,499.71	50,796.46	28.60
31	JHARKHAND	42	70,673.40	68,776.10	-2.68	12	23,623.12	29,539.75	25.05
32	UTTARAKHAND	32	34,539.29	46,325.58	34.12	10	25,404.50	37,217.29	46.50
33	TELANGANA	47	36,326.25	39,359.69	8.35	10	15,929.81	19,457.47	22.15
34	MULTI STATE	128	3,66,425.54	4,81,291.29	31.35	74	1,39,191.76	2,56,799.35	84.49
Total		1737	22,33,409.53	26,71,440.77	19.61	470	7,74,185.41	12,53,567.06	61.92

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-7

Extent of time overrun in projects with respect to original schedule						Rs. 150 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	4	67,120.00	80,348.00	36 - 145
2	CIVIL AVIATION	19	13,786.34	14,264.62	3.47	14	10,594.27	10,938.49	5 - 33
3	COAL	101	1,45,653.01	1,44,995.00	-0.45	52	69,856.32	64,315.47	8 - 228
4	FINANCE	2	557.77	557.73	-0.01	1	209.00	208.96	21 - 21
5	FERTILISERS	4	1,101.28	1,101.28	0.00	4	1,101.28	1,101.28	15 - 18
6	MINES	5	7,078.62	7,075.17	-0.05	2	6,023.00	6,023.00	20 - 23
7	STEEL	9	25,452.51	31,567.51	24.03	6	21,626.09	27,741.09	12 - 74
8	PETROLEUM	139	2,96,976.45	3,04,256.68	2.45	78	1,38,069.09	1,45,020.47	2 - 110
9	POWER	78	2,95,137.42	3,67,699.63	24.59	43	1,82,770.04	2,38,945.07	4 - 155
10	HEAVY INDUSTRY	1	1,554.00	900.00	-42.08	0	0.00	0.00	-
11	HEALTH AND FAMILY WELFARE	29	15,273.26	15,628.51	2.33	10	4,311.38	4,053.84	11 - 90
12	RAILWAYS	312	4,62,095.03	7,00,076.37	51.50	148	1,93,860.66	3,18,478.11	2 - 324
13	ROAD TRANSPORT AND HIGHWAYS	908	5,40,947.36	5,61,176.00	3.74	118	65,750.54	70,242.14	1 - 128
14	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	-
15	TELECOMMUNICATIONS	3	14,013.36	25,343.36	80.85	3	14,013.36	25,343.36	5 - 72
16	URBAN DEVELOPMENT	33	2,82,500.28	3,05,097.88	8.00	9	1,01,655.47	1,18,150.25	4 - 98
17	WATER RESOURCES	49	26,781.06	72,049.94	169.03	13	13,468.61	58,803.22	4 - 25
18	DEFENCE PRODUCTION	1	246.31	210.00	-14.74	1	246.31	210.00	22 - 22
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	-
20	HUMAN RESOURCE DEVELOPMENT	26	11,077.40	11,265.83	1.70	12	5,494.51	5,511.84	3 - 63
21	HOME AFFAIRS	5	1,993.40	2,849.31	42.94	2	1,382.09	2,238.00	26 - 44
22	RURAL DEVELOPMENT	4	889.43	899.87	1.17	3	527.83	538.27	58 - 70
23	CULTURE DEVELOPMENT	1	151.33	151.33	0.00	0	0.00	0.00	-
24	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	22 - 24
Total		1737	22,33,409.53	26,71,440.77	19.61	525	9,15,431.94	11,97,201.16	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-8

Extent of time overrun in projects with respect to original schedule(State Wise) (All Cost/ Expenditure in Rs. crore)						Rs.	150	Crore and above	
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Antici pated cost	Cost overrun (%)	No.	Original Cost	Antici pated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	77	1,22,880.98	1,70,411.65	38.68	24	86,247.24	1,32,284.73	1 - 180
2	ARUNACHAL PRADESH	42	24,624.65	44,366.68	80.17	2	7,538.43	21,245.53	60 - 155
3	ASSAM	47	42,046.33	45,563.88	8.37	13	8,699.04	11,182.60	2 - 63
4	BIHAR	108	1,22,099.62	1,58,462.50	29.78	23	38,178.73	64,173.04	4 - 141
5	GOA	11	5,629.77	5,640.26	0.19	0	0.00	0.00	-
6	GUJARAT	59	1,06,069.60	1,17,304.95	10.59	12	29,299.67	39,621.46	3 - 132
7	HARYANA	43	30,316.35	32,837.14	8.32	14	10,407.71	11,012.86	5 - 114
8	HIMACHAL PRADESH	15	20,365.24	30,249.67	48.54	3	6,665.52	12,643.52	11 - 154
9	JAMMU AND KASHMIR	22	40,412.13	66,473.44	64.49	2	10,612.12	36,061.12	63 - 241
10	KARNATAKA	60	71,320.53	80,896.72	13.43	17	40,828.50	45,898.03	2 - 264
11	KERALA	22	37,466.85	42,584.93	13.66	8	12,052.00	13,818.46	4 - 53
12	MADHYA PRADESH	84	91,161.40	1,04,808.86	14.97	41	31,885.94	38,588.47	6 - 73
13	MAHARASHTRA	242	2,17,334.38	2,41,218.69	10.99	45	60,702.23	83,935.03	5 - 216
14	MANIPUR	12	8,137.49	15,887.67	95.24	2	4,971.74	12,721.92	36 - 153
15	MEGHALAYA	7	3,245.09	6,563.59	102.26	1	363.99	363.99	43 - 43
16	MIZORAM	18	9,030.03	12,978.73	43.73	12	7,133.21	10,713.65	43 - 128
17	NAGALAND	38	18,265.97	22,463.91	22.98	14	6,473.72	10,762.04	38 - 117
18	ODISHA	89	1,29,891.78	1,34,147.04	3.28	34	71,209.88	74,543.04	3 - 228
19	PUNJAB	29	15,325.05	18,249.98	19.09	11	4,955.06	4,825.79	3 - 108
20	RAJASTHAN	60	53,090.50	61,137.54	15.16	11	19,321.37	24,625.61	3 - 75
21	SIKKIM	14	5,074.99	12,994.31	156.05	3	500.14	1,099.57	94 - 100
22	TAMIL NADU	71	1,19,185.26	1,38,369.59	16.10	25	65,777.71	75,280.05	3 - 198
23	TRIPURA	13	3,479.87	3,626.40	4.21	6	1,707.64	1,854.17	11 - 70
24	UTTAR PRADESH	134	1,78,012.58	1,85,467.12	4.19	32	54,110.70	54,309.16	2 - 68
25	WEST BENGAL	75	65,583.67	84,487.51	28.82	30	29,978.08	38,121.12	4 - 324
26	A & N ISLANDS	9	2,888.63	3,159.99	9.39	1	417.23	707.73	33 - 33
27	CHANDIGARH	2	349.15	570.00	63.25	0	0.00	0.00	-
28	DELHI	36	90,723.12	92,153.92	1.58	16	50,932.04	52,123.75	4 - 90
29	PONDICHERRY	1	195.00	195.00	0.00	1	195.00	195.00	19 - 19
30	CHHATISGARH	48	91,239.04	1,02,416.44	12.25	20	31,146.74	40,844.72	15 - 96
31	JHARKHAND	42	70,673.40	68,776.10	-2.68	19	53,677.79	47,078.45	12 - 152
32	UTTARAKHAND	32	34,539.29	46,325.58	34.12	5	22,303.02	33,060.80	3 - 126
33	TELANGANA	47	36,326.25	39,359.69	8.35	13	15,832.05	17,095.15	9 - 168
34	MULTI STATE	128	3,66,425.54	4,81,291.29	31.35	65	1,31,307.70	1,86,410.60	5 - 276
Total		1737	22,33,409.53	26,71,440.77	19.61	525	9,15,431.94	11,97,201.16	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-9

<u>Extent of time overrun in projects with respect to latest schedule</u>						Rs. 150 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	69,305.00	80,348.00	15.93	4	69,305.00	80,348.00	36 - 145
2	CIVIL AVIATION	19	14,124.25	14,264.62	0.99	11	8,942.47	8,858.78	5 - 33
3	COAL	101	1,47,446.06	1,44,995.00	-1.66	45	37,976.74	39,006.71	0 - 168
4	FINANCE	2	557.77	557.73	-0.01	1	209.00	208.96	21 - 21
5	FERTILISERS	4	1,101.28	1,101.28	0.00	1	426.72	426.72	15 - 15
6	MINES	5	7,971.07	7,075.17	-11.24	0	0.00	0.00	-
7	STEEL	9	31,867.51	31,567.51	-0.94	2	526.23	526.23	12 - 26
8	PETROLEUM	139	3,15,011.41	3,04,256.68	-3.41	25	23,068.55	22,019.98	2 - 38
9	POWER	78	3,57,073.75	3,67,699.63	2.98	22	1,13,953.58	1,14,260.35	5 - 126
10	HEAVY INDUSTRY	1	1,554.00	900.00	-42.08	0	0.00	0.00	-
11	HEALTH AND FAMILY WELFARE	29	15,273.26	15,628.51	2.33	10	4,311.38	4,053.84	11 - 90
12	RAILWAYS	312	5,30,373.10	7,00,076.37	32.00	122	1,69,446.96	2,75,218.22	2 - 324
13	ROAD TRANSPORT AND HIGHWAYS	908	5,42,881.78	5,61,176.00	3.37	91	52,376.09	54,574.68	0 - 128
14	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	-
15	TELECOMMUNICATIONS	3	14,013.20	25,343.36	80.85	3	14,013.20	25,343.36	5 - 72
16	URBAN DEVELOPMENT	33	2,86,942.00	3,05,097.88	6.33	8	1,05,523.45	1,17,728.25	9 - 98
17	WATER RESOURCES	49	72,273.40	72,049.94	-0.31	11	58,292.31	58,292.31	4 - 25
18	DEFENCE PRODUCTION	1	246.31	210.00	-14.74	1	246.31	210.00	22 - 22
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	-
20	HUMAN RESOURCE DEVELOPMENT	26	11,090.22	11,265.83	1.58	12	5,494.33	5,511.84	3 - 63
21	HOME AFFAIRS	5	2,068.54	2,849.31	37.75	1	1,219.21	2,000.00	26 - 26
22	RURAL DEVELOPMENT	4	968.31	899.87	-7.07	3	606.71	538.27	58 - 70
23	CULTURE DEVELOPMENT	1	151.33	151.33	0.00	0	0.00	0.00	-
24	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	22 - 24
Total		1737	24,45,317.46	26,71,440.77	9.25	375	6,83,290.33	8,28,116.80	

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-10

Extent of cost overrun in projects with respect to latest cost						Rs.	150	Crore and above	
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	69,305.00	80,348.00	15.93	3	29,456.00	40,499.00	37.49
2	CIVIL AVIATION	19	14,124.25	14,264.62	0.99	2	1,488.27	1,712.33	15.06
3	COAL	101	1,47,446.06	1,44,995.00	-1.66	14	23,571.99	27,530.00	16.79
4	FINANCE	2	557.77	557.73	-0.01	0	0.00	0.00	0.00
5	FERTILISERS	4	1,101.28	1,101.28	0.00	0	0.00	0.00	0.00
6	MINES	5	7,971.07	7,075.17	-11.24	0	0.00	0.00	0.00
7	STEEL	9	31,867.51	31,567.51	-0.94	0	0.00	0.00	0.00
8	PETROLEUM	139	3,15,011.41	3,04,256.68	-3.41	5	5,842.93	6,717.34	14.97
9	POWER	78	3,57,073.75	3,67,699.63	2.98	13	79,757.19	92,456.42	15.92
10	HEAVY INDUSTRY	1	1,554.00	900.00	-42.08	0	0.00	0.00	0.00
11	HEALTH AND FAMILY WELFARE	29	15,273.26	15,628.51	2.33	12	5,589.39	6,287.30	12.49
12	RAILWAYS	312	5,30,373.10	7,00,076.37	32.00	194	1,93,591.27	3,76,212.69	94.33
13	ROAD TRANSPORT AND HIGHWAYS	908	5,42,881.78	5,61,176.00	3.37	157	1,07,213.14	1,32,093.27	23.21
14	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0.00
15	TELECOMMUNICATIONS	3	14,013.20	25,343.36	80.85	2	13,765.00	25,095.16	82.31
16	URBAN DEVELOPMENT	33	2,86,942.00	3,05,097.88	6.33	5	57,954.79	76,189.87	31.46
17	WATER RESOURCES	49	72,273.40	72,049.94	-0.31	2	913.57	924.74	1.22
18	DEFENCE PRODUCTION	1	246.31	210.00	-14.74	0	0.00	0.00	0.00
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	0.00
20	HUMAN RESOURCE DEVELOPMENT	26	11,090.22	11,265.83	1.58	5	2,022.63	2,240.41	10.77
21	HOME AFFAIRS	5	2,068.54	2,849.31	37.75	1	1,219.21	2,000.00	64.04
22	RURAL DEVELOPMENT	4	968.31	899.87	-7.07	0	0.00	0.00	0.00
23	CULTURE DEVELOPMENT	1	151.33	151.33	0.00	0	0.00	0.00	0.00
24	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	9.44
Total		1737	24,45,317.46	26,71,440.77	9.25	417	5,39,737.47	8,08,948.83	49.88

^ - Cost Overrun = Anticipated Cost minus Revised/Original Cost

TABLE-11

Extent of time & cost overrun in projects with respect to latest schedule&cost Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	69,305.00	80,348.00	15.93	3	29,456.00	40,499.00	74- 145
2	CIVIL AVIATION	19	14,124.25	14,264.62	0.99	0	0.00	0.00	0- 0
3	COAL	101	1,47,446.06	1,44,995.00	-1.66	10	3,165.56	4,331.59	12- 132
4	FINANCE	2	557.77	557.73	-0.01	0	0.00	0.00	0- 0
5	FERTILISERS	4	1,101.28	1,101.28	0.00	0	0.00	0.00	0- 0
6	MINES	5	7,971.07	7,075.17	-11.24	0	0.00	0.00	0- 0
7	STEEL	9	31,867.51	31,567.51	-0.94	0	0.00	0.00	0- 0
8	PETROLEUM	139	3,15,011.41	3,04,256.68	-3.41	1	543.91	652.10	16- 16
9	POWER	78	3,57,073.75	3,67,699.63	2.98	2	5,991.58	7,854.35	11- 126
10	HEAVY INDUSTRY	1	1,554.00	900.00	-42.08	0	0.00	0.00	0- 0
11	HEALTH AND FAMILY WELFARE	29	15,273.26	15,628.51	2.33	1	414.11	499.23	90- 90
12	RAILWAYS	312	5,30,373.10	7,00,076.37	32.00	82	1,19,078.67	2,30,617.17	2- 324
13	ROAD TRANSPORT AND HIGHWAYS	908	5,42,881.78	5,61,176.00	3.37	14	12,885.18	16,036.23	15- 128
14	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0- 0
15	TELECOMMUNICATIONS	3	14,013.20	25,343.36	80.85	2	13,765.00	25,095.16	5- 72
16	URBAN DEVELOPMENT	33	2,86,942.00	3,05,097.88	6.33	2	33,909.00	46,193.00	44- 98
17	WATER RESOURCES	49	72,273.40	72,049.94	-0.31	0	0.00	0.00	0- 0
18	DEFENCE PRODUCTION	1	246.31	210.00	-14.74	0	0.00	0.00	0- 0
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	0- 0
20	HUMAN RESOURCE DEVELOPMENT	26	11,090.22	11,265.83	1.58	2	790.00	849.68	25- 52
21	HOME AFFAIRS	5	2,068.54	2,849.31	37.75	1	1,219.21	2,000.00	26- 26
22	RURAL DEVELOPMENT	4	968.31	899.87	-7.07	0	0.00	0.00	0- 0
23	CULTURE DEVELOPMENT	1	151.33	151.33	0.00	0	0.00	0.00	0- 0
24	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	22- 24
Total		1737	24,45,317.46	26,71,440.77	9.25	122	2,38,570.31	3,93,617.81	

^ - Cost Overrun = Anticipated Cost minus Revised/Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-12

Extent of time & cost overrun in projects with respect to original schedule&cost Rs. 150 Crore and above						(All Cost/ Expenditure in Rs. crore)			
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	74- 145
2	CIVIL AVIATION	19	13,786.34	14,264.62	3.47	2	1,559.23	1,939.73	12- 33
3	COAL	101	1,45,653.01	1,44,995.00	-0.45	14	21,102.12	22,704.37	8- 132
4	FINANCE	2	557.77	557.73	-0.01	0	0.00	0.00	0- 0
5	FERTILISERS	4	1,101.28	1,101.28	0.00	0	0.00	0.00	0- 0
6	MINES	5	7,078.62	7,075.17	-0.05	0	0.00	0.00	0- 0
7	STEEL	9	25,452.51	31,567.51	24.03	1	15,525.00	21,940.00	74- 74
8	PETROLEUM	139	2,96,976.45	3,04,256.68	2.45	22	55,889.06	73,453.48	7- 110
9	POWER	78	2,95,137.42	3,67,699.63	24.59	16	1,05,387.95	1,63,636.33	11- 155
10	HEAVY INDUSTRY	1	1,554.00	900.00	-42.08	0	0.00	0.00	0- 0
11	HEALTH AND FAMILY WELFARE	29	15,273.26	15,628.51	2.33	1	414.11	499.23	90- 90
12	RAILWAYS	312	4,62,095.03	7,00,076.37	51.50	104	1,35,577.71	2,66,058.71	2- 324
13	ROAD TRANSPORT AND HIGHWAYS	908	5,40,947.36	5,61,176.00	3.74	26	17,445.14	23,041.67	1- 128
14	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0- 0
15	TELECOMMUNICATIONS	3	14,013.36	25,343.36	80.85	1	13,334.00	24,664.00	72- 72
16	URBAN DEVELOPMENT	33	2,82,500.28	3,05,097.88	8.00	3	60,314.14	76,888.12	44- 98
17	WATER RESOURCES	49	26,781.06	72,049.94	169.03	2	10,349.47	55,773.56	4- 25
18	DEFENCE PRODUCTION	1	246.31	210.00	-14.74	0	0.00	0.00	0- 0
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	0- 0
20	HUMAN RESOURCE DEVELOPMENT	26	11,077.40	11,265.83	1.70	2	790.18	849.68	25- 52
21	HOME AFFAIRS	5	1,993.40	2,849.31	42.94	2	1,382.09	2,238.00	26- 44
22	RURAL DEVELOPMENT	4	889.43	899.87	1.17	2	352.34	362.78	58- 70
23	CULTURE DEVELOPMENT	1	151.33	151.33	0.00	0	0.00	0.00	0- 0
24	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	22- 24
Total		1737	22,33,409.53	26,71,440.77	19.61	203	4,84,045.63	7,93,538.96	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-13

<u>List of projects completed/dropped/Frozen during current month</u>					Rs. 150	Crore and above	
(All Cost/ Expenditure in Rs. crore)							
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure

TABLE-14

List of projects added Rs. 150 Crore and above					(April 2021)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC

TABLE-15

Milestones (Cumulative due & achieved)	Rs. 150	Crore and above
Total	5908	
Achieved up to month	3075	

TABLE-16

<u>List of projects reporting additional delayed</u> Rs. 150 Crore and above							(April 2021)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>CIVIL AVIATION</u>						
1	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI AAI	951.28	951.28	10/2021	03/2022	07/2022	4
2	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II AAI	1,216.90	1,216.90	10/2022	10/2022	03/2023	5
3	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA AAI	458.00	458.00	03/2020	06/2021	12/2021	6
4	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT AAI	177.10	177.10	02/2020	06/2021	12/2021	6
	<u>COAL</u>						
5	BHATADI EXPANSION OC MINE WCL	304.52	729.86	03/2019	03/2026	09/2026	6
6	SONEPUR BAZARI (COMB) OCP (8.0 MTY) ECL	1,055.05	1,055.05	03/2018	03/2021	10/2021	7
7	JALAGAM VENGALA RAO OCP-II SCCL	447.06	473.22	03/2015	03/2022	03/2023	12
8	NILJAI EXPANSION (DEEP) OC (3.5 MTY) WCL	319.76	404.45	03/2022	03/2021	03/2022	12
9	NEW MAJRI UG TO OC WCL	295.56	496.38	03/2019	03/2025	09/2026	18
10	SINGHORI OC MINE WCL	205.49	205.49	03/2020	03/2020	09/2021	18
11	UKNI DEEP OC WCL	318.14	318.14	03/2021	03/2021	09/2022	18
12	BELLORA-NAIGAON DEEP OC WCL	252.71	252.71	03/2021	03/2021	09/2022	18
13	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) WCL	328.00	328.00	03/2021	03/2021	09/2023	30
14	KOLAR PIMPRI EXTENSION OC WCL	362.73	402.90	03/2020	03/2020	09/2022	30
	<u>FINANCE</u>						
15	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI CPWD	209.00	208.96	10/2019	04/2021	07/2021	3
	<u>FERTILISERS</u>						

List of projects reporting additional delayed Rs. 150 Crore and above (April 2021)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
16	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT NFL	215.92	215.92	11/2019	04/2021	05/2021	1
17	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY RCF	426.72	426.72	04/2020	05/2021	07/2021	2
	<u>STEEL</u>						
18	FORGED WHEEL PLANT RINL	1,682.85	1,682.85	09/2018	04/2021	06/2021	2
19	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL SAIL	262.87	262.87	06/2019	05/2021	08/2021	3
20	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E SAIL	263.36	263.36	09/2020	05/2021	09/2021	4
21	COKE OVEN BATTERY-5 RINL	2,858.00	2,558.00	12/2017	12/2020	12/2021	12
	<u>PETROLEUM</u>						
22	SEA WATER DESALINATION PLANT MANGALORE REFIN Central Sector Projects	581.00	637.00	03/2020	06/2021	07/2021	1
23	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY IOCL	315.00	315.00	12/2021	06/2021	08/2021	2
24	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA OIL	543.91	652.10	02/2020	04/2021	06/2021	2
25	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN OIL	224.75	222.21	08/2020	04/2021	06/2021	2
26	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR IOCL	1,823.00	3,027.90	03/2021	08/2021	12/2021	4
27	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 ONGC	650.82	624.35	03/2019	05/2021	09/2021	4
28	BSVI UPGRADE MANGALORE REFIN	1,810.00	1,810.00	12/2019	10/2021	02/2022	4
29	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II OIL	571.66	571.66	12/2019	04/2021	08/2021	4
30	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT GAIL	2,881.40	2,000.00	12/2020	05/2021	09/2021	4
31	ADDITIONAL FACILITIES AT MANMAD FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE IOCL	212.00	212.00	01/2021	04/2021	09/2021	5

<u>List of projects reporting additional delayed</u> Rs. 150 Crore and above (April 2021)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
32	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE IOCL	261.00	261.00	01/2021	04/2021	09/2021	5
33	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU IOCL	466.43	466.43	10/2020	08/2021	01/2022	5
34	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH IOCL	466.00	466.00	04/2021	07/2021	12/2021	5
35	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP IOCL	316.20	316.20	10/2021	10/2021	03/2022	5
36	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION ONGC	2,292.46	2,203.71	05/2021	05/2021	12/2021	7
37	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV ONGC	3,660.71	3,740.05	05/2021	05/2021	01/2022	8
38	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) ONGC	861.79	2,001.00	05/2013	03/2021	02/2022	11
39	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS ONGC Central Sector Projects	3,190.69	3,375.90	04/2018	05/2021	05/2022	12
40	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) OIL	406.00	406.00	10/2020	03/2021	03/2022	12
41	Fuel Quality Upgradation Project at Paradip Refinery IOCL	3,361.00	3,361.00	08/2021	08/2021	09/2022	13
42	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT BPCL	580.20	580.20	02/2021	05/2021	03/2023	22
	<u>POWER</u>						
43	EASTERN REGION STRENGTHENING SCHEME-XII PGCIL	522.29	546.36	11/2016	05/2021	06/2021	1
44	BRBCL-NABINAGAR TPP- JV (4X250 MW) NTPC	5,353.00	10,566.00	07/2012	06/2021	07/2021	1
45	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTRIC PGCIL	808.63	808.63	01/2018	04/2021	05/2021	1
46	EASTERN REGION STRENGTHENING SCHEME-XV PGCIL	454.11	454.11	04/2018	04/2021	05/2021	1
47	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) PGCIL	235.53	235.53	06/2019	05/2021	06/2021	1

List of projects reporting additional delayed Rs. 150 Crore and above							(April 2021)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
48	EASTERN REGION STRENGTHENING SCHEME- XVIII PGCIL Central Sector Projects	3,500.00	3,994.00	07/2020	05/2021	06/2021	1
49	EASTERN REGION STRENGTHENING SCHEME XX PGCIL	358.83	358.83	05/2020	04/2021	05/2021	1
50	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI CPWD	271.90	271.90	11/2019	05/2021	06/2021	1
51	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P PGCIL	14,733.37	14,733.37	11/2019	04/2021	06/2021	2
52	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY PGCIL Central Sector Projects	186.17	219.66	07/2019	04/2021	06/2021	2
53	DURGAPUR PP-III (2X20 MW) - NSPCL NTPC	529.68	529.68	11/2018	05/2021	07/2021	2
54	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) PGCIL	1,394.52	1,394.52	05/2017	06/2021	09/2021	3
55	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ PGCIL	322.30	322.30	02/2019	06/2021	09/2021	3
56	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII PGCIL	379.95	379.95	12/2019	06/2021	09/2021	3
57	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL NTPC	1,885.13	1,885.13	12/2018	03/2021	07/2021	4
	RAILWAYS						
58	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR NFR	1,180.19	4,541.38	12/2008	04/2021	05/2021	1
59	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF SR	931.98	1,121.00	N.A.	04/2021	05/2021	1
60	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) WR	829.74	1,959.74	03/2020	12/2023	03/2024	3
61	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) NWR	808.85	808.85	08/2022	06/2022	11/2022	5
62	PHULERA - DIGANA DOUBLING NWR	600.00	701.81	03/2020	04/2022	10/2022	6
63	DAUSA-GANGAPUR CITY(NL),NWR NWR	410.08	860.41	02/2019	11/2021	06/2022	7
64	KATNI - SINGRAULI DOUBLING PROJECT WCR	1,763.93	1,762.94	03/2020	03/2023	03/2024	12

List of projects reporting additional delayed Rs. 150 Crore and above							(April 2021)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
65	HUBLI- CHIKJAJUR SWR	1,156.94	1,656.00	03/2020	11/2021	03/2023	16
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
66	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS NHAI	364.56	392.00	N.A.	03/2021	04/2021	1
67	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU NHAI	1,166.26	1,296.93	N.A.	07/2021	08/2021	1
68	2L+PS OF THIKRI ANJAD SECTION OF NH-347B MoRTH	249.05	249.05	07/2018	03/2021	04/2021	1
69	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA MoRTH	169.63	169.63	03/2018	04/2021	06/2021	2
70	4-LANING OF BRAHAMPORE-FARAKA NHAI PPP (BOT)	998.79	998.79	08/2013	03/2022	06/2022	3
71	DELHI AGRA APPROVED LENGTH 180.0 KM NHAI PPP (BOT)	1,928.22	3,182.34	04/2015	03/2021	06/2021	3
72	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN NHAI	649.50	649.50	03/2019	12/2021	03/2022	3
73	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 MoRTH EPC	628.45	628.45	01/2020	03/2021	06/2021	3
74	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN NHAI	754.54	756.27	03/2020	09/2021	12/2021	3
75	FOUR LANING OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULAM (KM 7.300) TO NATHAM (KM. 3 NHAI EPC	505.35	505.35	N.A.	05/2021	08/2021	3
76	FOUR LANING OF MADURAI- CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300) NHAI EPC	628.71	628.71	N.A.	09/2021	12/2021	3
77	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS MoRTH	254.17	254.17	02/2018	03/2021	06/2021	3
78	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS MoRTH	279.44	279.44	03/2018	03/2021	06/2021	3
79	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA MoRTH	536.65	536.65	12/2019	03/2021	06/2021	3
80	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS NHAI	1,016.92	1,071.00	N.A.	07/2021	01/2022	6

List of projects reporting additional delayed Rs. 150 Crore and above (April 2021)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
81	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 MoRTH	1,069.59	1,069.59	10/2019	12/2020	08/2021	8
82	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD MoRTH	264.50	264.50	03/2021	03/2021	11/2021	8
83	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 NHAI	314.43	314.43	N.A.	06/2021	03/2022	9
TELECOMMUNICATIONS							
84	NETWORK FOR SPECTRUM DOT	13,334.00	24,664.00	07/2015	06/2021	07/2021	1
URBAN DEVELOPMENT							
85	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI CPWD	197.33	197.33	04/2019	10/2021	12/2021	2
DEFENCE PRODUCTION							
86	RESIDENTIAL QUARTERS FOR HAL,BANGLORE CPWD	246.31	210.00	02/2020	06/2021	12/2021	6
HUMAN RESOURCE DEVELOPMENT							
87	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB CPWD	294.00	350.69	04/2019	04/2021	05/2021	1
RURAL DEVELOPMENT							
88	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V HSCL	149.73	155.66	12/2015	03/2021	10/2021	7
89	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI HSCL	202.61	207.12	12/2016	03/2021	10/2021	7
90	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII HSCL	175.49	175.49	12/2016	03/2021	12/2021	9

TABLE-17

Sector wise analysis of projects Rs. 150 Crore and above					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	67,120.00	693,05.00	80,348.00	59,554.96
CIVIL AVIATION	19	13,786.34	141,24.25	14,264.62	4,197.34
COAL	101	1,45,653.01	1,474,46.06	1,44,995.00	49,331.74
FINANCE	2	557.77	5,57.77	557.73	329.71
FERTILISERS	4	1,101.28	11,01.28	1,101.28	847.51
MINES	5	7,078.62	79,71.07	7,075.17	1,301.06
STEEL	9	25,452.51	318,67.51	31,567.51	23,179.80
PETROLEUM	139	2,96,976.45	3,150,11.41	3,04,256.68	1,15,047.73
POWER	78	2,95,137.42	3,570,73.75	3,67,699.63	2,56,834.13
HEAVY INDUSTRY	1	1,554.00	15,54.00	900.00	815.00
HEALTH AND FAMILY WELFARE	29	15,273.26	152,73.26	15,628.51	7,898.83
RAILWAYS	312	4,62,095.03	5,303,73.10	7,00,076.37	2,50,483.48
ROAD TRANSPORT AND HIGHWAYS	908	5,40,947.36	5,428,81.78	5,61,176.00	3,51,797.31
SHIPPING AND PORTS	1	5,369.18	53,69.18	4,633.81	1,871.35
TELECOMMUNICATIONS	3	14,013.36	140,13.20	25,343.36	17,990.26
URBAN DEVELOPMENT	33	2,82,500.28	2,869,42.00	3,05,097.88	1,36,565.95
WATER RESOURCES	49	26,781.06	722,73.40	72,049.94	22,138.40
DEFENCE PRODUCTION	1	246.31	2,46.31	210.00	131.46
COMMERCE	1	302.64	3,02.64	302.64	60.00
HUMAN RESOURCE DEVELOPMENT	26	11,077.40	110,90.22	11,265.83	2,475.25
HOME AFFAIRS	5	1,993.40	20,68.54	2,849.31	1,088.12
RURAL DEVELOPMENT	4	889.43	9,68.31	899.87	472.48
CULTURE DEVELOPMENT	1	151.33	1,51.33	151.33	148.33
DPIIT	2	17,352.09	173,52.09	18,990.30	11,472.42
Grand total	1737	22,33,409.53	24,45,317.46	26,71,440.77	13,16,032.62

TABLE-18

State-Wise Position of Central Sector Projects costing Rs. 150 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	77	1,22,880.98	1,70,411.65	38.68	7	41,080.27	96,339.76	1 - 180
2	ARUNACHAL PRADESH	42	24,624.65	44,366.68	80.17	1	6,285.33	19,992.43	155 - 155
3	ASSAM	47	42,046.33	45,563.88	8.37	7	5,847.24	8,556.06	2 - 48
4	BIHAR	108	1,22,099.62	1,58,462.50	29.78	10	30,865.91	56,867.93	15 - 141
5	GOA	11	5,629.77	5,640.26	0.19	0	0.00	0.00	-
6	GUJARAT	59	1,06,069.60	1,17,304.95	10.59	9	27,063.50	37,513.07	3 - 132
7	HARYANA	43	30,316.35	32,837.14	8.32	3	828.42	1,520.46	7 - 114
8	HIMACHAL PRADESH	15	20,365.24	30,249.67	48.54	1	3,919.59	9,897.59	154 - 154
9	JAMMU AND KASHMIR	22	40,412.13	66,473.44	64.49	1	2,500.00	27,949.00	241 - 241
10	KARNATAKA	60	71,320.53	80,896.72	13.43	5	29,365.86	34,769.12	15 - 96
11	KERALA	22	37,466.85	42,584.93	13.66	4	7,431.46	9,221.96	32 - 53
12	MADHYA PRADESH	84	91,161.40	1,04,808.86	14.97	11	10,249.23	17,566.11	12 - 73
13	MAHARASHTRA	242	2,17,334.38	2,41,218.69	10.99	19	44,335.78	67,713.19	8 - 216
14	MANIPUR	12	8,137.49	15,887.67	95.24	1	4,454.17	12,264.15	153 - 153
15	MEGHALAYA	7	3,245.09	6,563.59	102.26	0	0.00	0.00	-
16	MIZORAM	18	9,030.03	12,978.73	43.73	4	2,969.16	6,549.60	81 - 128
17	NAGALAND	38	18,265.97	22,463.91	22.98	2	2,699.59	7,298.00	57 - 117
18	ODISHA	89	1,29,891.78	1,34,147.04	3.28	12	25,923.02	33,494.18	15 - 204
19	PUNJAB	29	15,325.05	18,249.98	19.09	2	1,048.54	1,106.96	21 - 25
20	RAJASTHAN	60	53,090.50	61,137.54	15.16	4	14,044.26	19,348.73	15 - 75
21	SIKKIM	14	5,074.99	12,994.31	156.05	3	500.14	1,099.57	94 - 100
22	TAMIL NADU	71	1,19,185.26	1,38,369.59	16.10	9	11,406.45	22,407.51	23 - 198
23	TRIPURA	13	3,479.87	3,626.40	4.21	3	921.97	1,104.78	24 - 70
24	UTTAR PRADESH	134	1,78,012.58	1,85,467.12	4.19	6	20,949.75	22,329.44	8 - 68
25	WEST BENGAL	75	65,583.67	84,487.51	28.82	11	17,317.29	25,480.93	4 - 324
26	A & N ISLANDS	9	2,888.63	3,159.99	9.39	1	417.23	707.73	33 - 33
27	CHANDIGARH	2	349.15	570.00	63.25	0	0.00	0.00	-
28	DELHI	36	90,723.12	92,153.92	1.58	3	6,406.32	7,677.23	24 - 90
29	PONDICHERRY	1	195.00	195.00	0.00	0	0.00	0.00	-
30	CHHATISGARH	48	91,239.04	1,02,416.44	12.25	9	25,751.75	35,569.08	21 - 84
31	JHARKHAND	42	70,673.40	68,776.10	-2.68	3	14,867.78	16,082.37	28 - 50
32	UTTARAKHAND	32	34,539.29	46,325.58	34.12	3	21,686.06	32,443.84	3 - 126
33	TELANGANA	47	36,326.25	39,359.69	8.35	7	12,777.27	14,151.63	9 - 132
34	MULTI STATE	128	3,66,425.54	4,81,291.29	31.35	42	90,132.29	1,46,516.55	9 - 276
Total		1737	22,33,409.53	26,71,440.77	19.61	203	4,84,045.63	7,93,538.96	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-19

EXECUTIVE SUMMARY COSTING Rs. 1000 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	161	5
2	ROAD TRANSPORT AND HIGHWAYS	156	4
3	PETROLEUM	57	8
4	POWER	46	5
5	COAL	30	1
6	URBAN DEVELOPMENT	23	0
7	CIVIL AVIATION	5	1
8	STEEL	5	2
9	ATOMIC ENERGY	4	0
10	HEALTH AND FAMILY WELFARE	4	0
11	DPIIT	2	0
12	MINES	1	0
13	SHIPPING AND PORTS	1	0
14	TELECOMMUNICATIONS	1	1
15	WATER RESOURCES	1	0
16	HOME AFFAIRS	1	0
	Total	498	27

TABLE-20

Month wise List of Completed Projects Costing Rs. 1000 crore and above during				
2021-2022				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)

TABLE-21

Month wise List of Deleted Projects Costing Rs. 1000 crore and above during				
2021-2022				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)

TABLE-22

Projects Added / Completed / Dropped / Frozen Rs. 1000 Crore and above

No of Projects in Previous Month	498
No of Projects Completed/Dropped/Frozen in Current Month	0
No of Projects added in Current Month	0
No of Projects in Current Month	498

Project status Rs. 1000 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	205 (41.16%)	9 (1.81%)	70 (14.06%)	34 (6.83%)	180 (36.14%)	498
Latest Approved (Date)	139 (27.91%)	11 (2.21%)	136 (27.31%)	32 (6.43%)	180 (36.14%)	498

Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	416	13,66,861.80	15,80,012.28	7,28,288.76	46.10	2,13,150.48	15.60
Project with Revision in Cost	82	5,62,741.96	5,71,056.09	3,21,862.67	56.40	8,314.13	1.50
Total	498	19,29,603.76	21,51,068.37	10,50,151.43	48.82	2,21,464.61	11.48
Original Cost of All Projects							
Original Cost	498	17,21,591.41	21,51,068.37	10,50,151.43	48.82	4,29,476.96	24.95

Delayed Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	205	7,72,122.30	10,56,187.48	6,15,399.96	58.30	2,84,065.18	36.79
Latest Approved (RCE)	139	5,82,571.92	7,26,643.07	4,10,220.46	56.50	1,44,071.15	24.73

Additional Delayed Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Latest Approved	27	77,937.64	1,02,930.30	76,599.60	74.40	24,992.66	32.10
Total	27	77,937.64	1,02,930.30	76,599.60	74.42	24,992.66	32.07

TABLE-23

Extent of cost overrun in projects with respect to original cost (Sector Wise)						Rs. 1000 Crore and above			
						(All Cost/ Expenditure in Rs. crore)			
						Projects with cost overrun [^]			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	48.51
2	CIVIL AVIATION	5	7,613.90	7,703.90	1.18	1	1,142.00	1,232.00	7.88
3	COAL	30	1,08,556.34	1,13,115.57	4.20	3	25,805.84	30,365.07	17.67
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
5	STEEL	5	24,006.86	30,121.86	25.47	1	15,525.00	21,940.00	41.32
6	PETROLEUM	57	2,64,239.96	2,71,220.92	2.64	16	58,110.61	76,388.51	31.45
7	POWER	46	2,81,387.51	3,53,015.51	25.46	24	1,71,424.92	2,45,126.27	42.99
8	HEALTH AND FAMILY WELFARE	4	6,160.00	6,531.00	6.02	2	2,928.00	3,299.00	12.67
9	RAILWAYS	161	3,94,274.15	6,24,000.70	58.27	121	1,98,375.92	4,29,387.46	116.45
10	ROAD TRANSPORT AND HIGHWAYS	156	2,36,631.03	2,52,551.93	6.73	44	59,229.74	76,546.89	29.24
11	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0.00
12	TELECOMMUNICATIONS	1	13,334.00	24,664.00	84.97	1	13,334.00	24,664.00	84.97
13	URBAN DEVELOPMENT	23	2,78,636.14	3,01,082.00	8.06	6	84,359.93	1,06,884.99	26.70
14	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	447.22
15	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	64.04
16	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	9.44
Total		498	17,21,591.41	21,51,068.37	24.95	226	6,86,229.30	11,32,872.36	65.09

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-24

Extent of cost overrun in projects with respect to original cost (State Wise) Rs.						1000 Crore and above			
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun[^]			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	22	1,00,790.37	1,48,161.40	47.00	10	45,532.51	1,02,125.54	124.29
2	ARUNACHAL PRADESH	5	13,732.92	32,928.36	139.78	3	10,761.23	29,956.67	178.38
3	ASSAM	6	27,224.48	29,692.21	9.06	4	4,630.48	7,098.21	53.29
4	BIHAR	27	87,426.57	1,21,814.59	39.33	15	33,512.04	67,900.06	102.61
5	GUJARAT	24	87,824.17	98,441.87	12.09	10	30,646.76	41,923.51	36.80
6	HARYANA	12	16,498.78	18,358.28	11.27	1	1,108.00	2,967.50	167.82
7	HIMACHAL PRADESH	8	17,307.75	27,192.18	57.11	3	8,237.58	18,122.01	119.99
8	JAMMU AND KASHMIR	14	37,748.07	63,675.32	68.69	3	6,236.00	32,296.00	417.90
9	KARNATAKA	17	53,661.87	62,706.98	16.86	10	40,753.66	49,798.77	22.19
10	KERALA	11	32,478.92	37,206.00	14.55	8	16,604.02	21,355.14	28.61
11	MADHYA PRADESH	23	61,740.86	74,374.58	20.46	11	31,854.48	45,006.24	41.29
12	MAHARASHTRA	49	1,39,827.20	1,66,198.89	18.86	20	57,187.57	84,266.19	47.35
13	MANIPUR	1	4,454.17	12,264.15	175.34	1	4,454.17	12,264.15	175.34
14	MEGHALAYA	1	906.46	4,083.02	350.44	1	906.46	4,083.02	350.44
15	MIZORAM	1	2,393.47	5,521.45	130.69	1	2,393.47	5,521.45	130.69
16	NAGALAND	3	7,896.52	12,481.00	58.06	1	2,326.52	6,911.00	197.05
17	ODISHA	37	1,04,138.78	1,12,178.14	7.72	11	26,251.24	34,290.60	30.62
18	PUNJAB	4	5,049.00	7,181.59	42.24	2	2,557.95	4,867.50	90.29
19	RAJASTHAN	15	31,995.25	38,670.71	20.86	5	16,355.72	23,031.18	40.81
20	SIKKIM	1	1,339.48	8,600.00	542.04	1	1,339.48	8,600.00	542.04
21	TAMIL NADU	27	99,664.04	1,17,838.13	18.24	14	37,271.47	55,840.56	49.82
22	UTTAR PRADESH	48	1,40,935.26	1,47,900.58	4.94	14	48,992.89	56,899.34	16.14
23	WEST BENGAL	25	47,280.10	65,048.81	37.58	14	25,352.53	43,152.57	70.21
24	DELHI	9	80,186.38	81,749.70	1.95	3	10,256.21	11,898.73	16.01
25	CHHATISGARH	18	77,851.94	88,489.77	13.66	8	37,748.96	48,488.81	28.45
26	JHARKHAND	16	56,545.31	60,442.40	6.89	6	21,917.94	27,371.03	24.88
27	UTTARAKHAND	6	26,039.84	37,071.69	42.37	4	23,213.06	34,244.91	47.52
28	TELANGANA	6	19,991.02	22,099.10	10.55	3	12,977.58	15,453.54	19.08
29	MULTI STATE	62	3,38,662.43	4,48,697.47	32.49	39	1,24,849.32	2,37,138.13	89.94
Total		498	17,21,591.41	21,51,068.37	24.95	226	6,86,229.30	11,32,872.36	65.09

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-25

Extent of time overrun in projects with respect to original schedule Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	4	67,120.00	80,348.00	36 - 145
2	CIVIL AVIATION	5	7,613.90	7,703.90	1.18	4	6,208.90	6,298.90	5 - 12
3	COAL	30	1,08,556.34	1,13,115.57	4.20	13	48,174.85	48,175.65	8 - 228
4	MINES	1	5,540.00	5,540.00	0.00	1	5,540.00	5,540.00	20 - 20
5	STEEL	5	24,006.86	30,121.86	25.47	4	21,099.86	27,214.86	33 - 74
6	PETROLEUM	57	2,64,239.96	2,71,220.92	2.64	28	1,18,966.84	1,25,764.03	5 - 110
7	POWER	46	2,81,387.51	3,53,015.51	25.46	27	1,76,076.47	2,32,193.94	4 - 155
8	HEALTH AND FAMILY WELFARE	4	6,160.00	6,531.00	6.02	0	0.00	0.00	-
9	RAILWAYS	161	3,94,274.15	6,24,000.70	58.27	100	1,65,657.03	2,88,502.53	2 - 324
10	ROAD TRANSPORT AND HIGHWAYS	156	2,36,631.03	2,52,551.93	6.73	14	21,142.87	24,372.48	1 - 105
11	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	-
12	TELECOMMUNICATIONS	1	13,334.00	24,664.00	84.97	1	13,334.00	24,664.00	72 - 72
13	URBAN DEVELOPMENT	23	2,78,636.14	3,01,082.00	8.06	5	1,00,079.14	1,16,573.92	41 - 98
14	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	25 - 25
15	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	26 - 26
16	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	22 - 24
Total		498	17,21,591.41	21,51,068.37	24.95	205	7,72,122.30	10,56,187.48	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-26

Extent of time overrun in projects with respect to original schedule(State Wise)						Rs.	1000	Crore and above	
(All Cost/ Expenditure in Rs. crore)						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	22	1,00,790.37	1,48,161.40	47.00	10	80,449.98	1,26,487.47	1 - 180
2	ARUNACHAL PRADESH	5	13,732.92	32,928.36	139.78	2	7,538.43	21,245.53	60 - 155
3	ASSAM	6	27,224.48	29,692.21	9.06	4	4,630.48	7,098.21	2 - 48
4	BIHAR	27	87,426.57	1,21,814.59	39.33	10	33,252.42	58,706.95	5 - 141
5	GUJARAT	24	87,824.17	98,441.87	12.09	7	26,970.60	36,965.18	3 - 74
6	HARYANA	12	16,498.78	18,358.28	11.27	3	6,046.66	6,046.66	7 - 29
7	HIMACHAL PRADESH	8	17,307.75	27,192.18	57.11	2	6,405.52	12,383.52	15 - 154
8	JAMMU AND KASHMIR	14	37,748.07	63,675.32	68.69	2	10,612.12	36,061.12	63 - 241
9	KARNATAKA	17	53,661.87	62,706.98	16.86	5	33,596.70	38,385.74	26 - 264
10	KERALA	11	32,478.92	37,206.00	14.55	5	10,744.46	12,510.92	15 - 53
11	MADHYA PRADESH	23	61,740.86	74,374.58	20.46	13	19,338.26	25,650.22	12 - 73
12	MAHARASHTRA	49	1,39,827.20	1,66,198.89	18.86	16	48,722.86	70,877.41	7 - 216
13	MANIPUR	1	4,454.17	12,264.15	175.34	1	4,454.17	12,264.15	153 - 153
14	MEGHALAYA	1	906.46	4,083.02	350.44	0	0.00	0.00	-
15	MIZORAM	1	2,393.47	5,521.45	130.69	1	2,393.47	5,521.45	108 - 108
16	NAGALAND	3	7,896.52	12,481.00	58.06	1	2,326.52	6,911.00	117 - 117
17	ODISHA	37	1,04,138.78	1,12,178.14	7.72	22	60,605.50	67,986.03	5 - 228
18	PUNJAB	4	5,049.00	7,181.59	42.24	1	1,069.59	1,069.59	22 - 22
19	RAJASTHAN	15	31,995.25	38,670.71	20.86	3	15,624.71	20,383.71	4 - 75
20	SIKKIM	1	1,339.48	8,600.00	542.04	0	0.00	0.00	-
21	TAMIL NADU	27	99,664.04	1,17,838.13	18.24	12	58,442.91	68,096.08	3 - 145
22	UTTAR PRADESH	48	1,40,935.26	1,47,900.58	4.94	13	46,898.56	47,298.55	4 - 48
23	WEST BENGAL	25	47,280.10	65,048.81	37.58	12	23,827.27	31,756.93	12 - 324
24	DELHI	9	80,186.38	81,749.70	1.95	5	47,151.73	48,258.32	24 - 66
25	CHHATISGARH	18	77,851.94	88,489.77	13.66	6	25,403.02	34,561.43	21 - 74
26	JHARKHAND	16	56,545.31	60,442.40	6.89	7	43,801.65	43,268.49	13 - 83
27	UTTARAKHAND	6	26,039.84	37,071.69	42.37	3	21,686.06	32,443.84	3 - 126
28	TELANGANA	6	19,991.02	22,099.10	10.55	2	11,759.46	12,158.18	20 - 168
29	MULTI STATE	62	3,38,662.43	4,48,697.47	32.49	37	1,18,369.19	1,71,790.80	6 - 276
Total		498	17,21,591.41	21,51,068.37	24.95	205	7,72,122.30	10,56,187.48	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-27

Extent of time overrun in projects with respect to latest schedule						Rs. 1000 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	69,305.00	80,348.00	15.93	4	69,305.00	80,348.00	36 - 145
2	CIVIL AVIATION	5	7,613.90	7,703.90	1.18	3	5,066.90	5,066.90	5 - 12
3	COAL	30	1,10,630.02	1,13,115.57	2.25	9	24,640.15	24,640.15	0 - 168
4	MINES	1	6,435.90	5,540.00	-13.92	0	0.00	0.00	-
5	STEEL	5	30,421.86	30,121.86	-0.99	0	0.00	0.00	-
6	PETROLEUM	57	2,81,800.41	2,71,220.92	-3.75	6	16,055.10	15,149.66	5 - 33
7	POWER	46	3,42,897.91	3,53,015.51	2.95	12	1,10,046.32	1,10,353.09	11 - 126
8	HEALTH AND FAMILY WELFARE	4	6,160.00	6,531.00	6.02	0	0.00	0.00	-
9	RAILWAYS	161	4,62,128.90	6,24,000.70	35.03	82	1,46,024.91	2,51,434.70	2 - 324
10	ROAD TRANSPORT AND HIGHWAYS	156	2,36,460.39	2,52,551.93	6.81	13	19,610.25	21,873.48	15 - 105
11	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	-
12	TELECOMMUNICATIONS	1	13,334.00	24,664.00	84.97	1	13,334.00	24,664.00	72 - 72
13	URBAN DEVELOPMENT	23	2,82,926.12	3,01,082.00	6.42	5	1,04,369.12	1,16,573.92	41 - 98
14	WATER RESOURCES	1	55,548.87	55,548.87	0.00	1	55,548.87	55,548.87	25 - 25
15	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	26 - 26
16	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	22 - 24
Total		498	19,29,603.76	21,51,068.37	11.48	139	5,82,571.92	7,26,643.07	

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-28

<u>Extent of cost overrun in projects with respect to latest cost</u>						Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)			
						Projects with cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	69,305.00	80,348.00	15.93	3	29,456.00	40,499.00	37.49
2	CIVIL AVIATION	5	7,613.90	7,703.90	1.18	1	1,142.00	1,232.00	7.88
3	COAL	30	1,10,630.02	1,13,115.57	2.25	2	19,898.73	22,384.28	12.49
4	MINES	1	6,435.90	5,540.00	-13.92	0	0.00	0.00	0.00
5	STEEL	5	30,421.86	30,121.86	-0.99	0	0.00	0.00	0.00
6	PETROLEUM	57	2,81,800.41	2,71,220.92	-3.75	2	4,523.46	5,073.00	12.15
7	POWER	46	3,42,897.91	3,53,015.51	2.95	10	78,418.09	90,609.04	15.55
8	HEALTH AND FAMILY WELFARE	4	6,160.00	6,531.00	6.02	2	2,928.00	3,299.00	12.67
9	RAILWAYS	161	4,62,128.90	6,24,000.70	35.03	108	1,63,719.13	3,29,051.92	100.99
10	ROAD TRANSPORT AND HIGHWAYS	156	2,36,460.39	2,52,551.93	6.81	47	63,357.74	80,713.51	27.39
11	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0.00
12	TELECOMMUNICATIONS	1	13,334.00	24,664.00	84.97	1	13,334.00	24,664.00	84.97
13	URBAN DEVELOPMENT	23	2,82,926.12	3,01,082.00	6.42	5	57,954.79	76,189.87	31.46
14	WATER RESOURCES	1	55,548.87	55,548.87	0.00	0	0.00	0.00	0.00
15	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	64.04
16	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	9.44
Total		498	19,29,603.76	21,51,068.37	11.48	184	4,53,303.24	6,94,705.92	53.25

^ - Cost Overrun = Anticipated Cost minus Revised/Original Cost

TABLE-29

Extent of time & cost overrun in projects with respect to latest schedule&cost Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	69,305.00	80,348.00	15.93	3	29,456.00	40,499.00	74- 145
2	CIVIL AVIATION	5	7,613.90	7,703.90	1.18	0	0.00	0.00	0- 0
3	COAL	30	1,10,630.02	1,13,115.57	2.25	0	0.00	0.00	0- 0
4	MINES	1	6,435.90	5,540.00	-13.92	0	0.00	0.00	0- 0
5	STEEL	5	30,421.86	30,121.86	-0.99	0	0.00	0.00	0- 0
6	PETROLEUM	57	2,81,800.41	2,71,220.92	-3.75	0	0.00	0.00	0- 0
7	POWER	46	3,42,897.91	3,53,015.51	2.95	2	5,991.58	7,854.35	11- 126
8	HEALTH AND FAMILY WELFARE	4	6,160.00	6,531.00	6.02	0	0.00	0.00	0- 0
9	RAILWAYS	161	4,62,128.90	6,24,000.70	35.03	60	1,08,774.84	2,15,469.62	2- 324
10	ROAD TRANSPORT AND HIGHWAYS	156	2,36,460.39	2,52,551.93	6.81	5	8,142.83	10,406.06	15- 105
11	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0- 0
12	TELECOMMUNICATIONS	1	13,334.00	24,664.00	84.97	1	13,334.00	24,664.00	72- 72
13	URBAN DEVELOPMENT	23	2,82,926.12	3,01,082.00	6.42	2	33,909.00	46,193.00	44- 98
14	WATER RESOURCES	1	55,548.87	55,548.87	0.00	0	0.00	0.00	0- 0
15	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	26- 26
16	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	22- 24
Total		498	19,29,603.76	21,51,068.37	11.48	76	2,18,179.55	3,66,076.33	

^ - Cost Overrun = Anticipated Cost minus Revised/Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-30

Extent of time & cost overrun in projects with respect to original schedule&cost Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	74- 145
2	CIVIL AVIATION	5	7,613.90	7,703.90	1.18	1	1,142.00	1,232.00	12- 12
3	COAL	30	1,08,556.34	1,13,115.57	4.20	1	17,237.00	17,237.80	8- 8
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
5	STEEL	5	24,006.86	30,121.86	25.47	1	15,525.00	21,940.00	74- 74
6	PETROLEUM	57	2,64,239.96	2,71,220.92	2.64	14	53,088.34	70,190.72	8- 110
7	POWER	46	2,81,387.51	3,53,015.51	25.46	14	1,04,679.49	1,62,870.31	11- 155
8	HEALTH AND FAMILY WELFARE	4	6,160.00	6,531.00	6.02	0	0.00	0.00	0- 0
9	RAILWAYS	161	3,94,274.15	6,24,000.70	58.27	74	1,21,438.63	2,45,569.12	2- 324
10	ROAD TRANSPORT AND HIGHWAYS	156	2,36,631.03	2,52,551.93	6.73	6	9,675.45	12,905.06	1- 105
11	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0- 0
12	TELECOMMUNICATIONS	1	13,334.00	24,664.00	84.97	1	13,334.00	24,664.00	72- 72
13	URBAN DEVELOPMENT	23	2,78,636.14	3,01,082.00	8.06	3	60,314.14	76,888.12	44- 98
14	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	25- 25
15	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	26- 26
16	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	22- 24
Total		498	17,21,591.41	21,51,068.37	24.95	122	4,52,427.39	7,50,535.30	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-31

<u>List of projects completed/dropped/Frozen during current month</u>							
Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)							
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure

TABLE-32

List of projects added Rs. 1000 Crore and above							(April 2021)
			Original		Anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	

TABLE-33

Milestones (Cumulative due & achieved)	Rs. 1000	Crore and above
Total	2854	
Achieved up to month	1864	

TABLE-34

List of projects reporting additional delayed Rs. 1000 Crore and above							(April 2021)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>CIVIL AVIATION</u>						
1	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II AAI	1,216.90	1,216.90	10/2022	10/2022	03/2023	5
	<u>COAL</u>						
2	SONEPUR BAZARI (COMB) OCP (8.0 MTY) ECL	1,055.05	1,055.05	03/2018	03/2021	10/2021	7
	<u>STEEL</u>						
3	FORGED WHEEL PLANT RINL	1,682.85	1,682.85	09/2018	04/2021	06/2021	2
4	COKE OVEN BATTERY-5 RINL	2,858.00	2,558.00	12/2017	12/2020	12/2021	12
	<u>PETROLEUM</u>						
5	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR IOCL	1,823.00	3,027.90	03/2021	08/2021	12/2021	4
6	BSVI UPGRADATION MANGALORE REFIN	1,810.00	1,810.00	12/2019	10/2021	02/2022	4
7	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT GAIL	2,881.40	2,000.00	12/2020	05/2021	09/2021	4
8	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION ONGC	2,292.46	2,203.71	05/2021	05/2021	12/2021	7
9	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV ONGC	3,660.71	3,740.05	05/2021	05/2021	01/2022	8
10	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) ONGC	861.79	2,001.00	05/2013	03/2021	02/2022	11
11	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS ONGC Central Sector Projects	3,190.69	3,375.90	04/2018	05/2021	05/2022	12
12	Fuel Quality Upgradation Project at Paradip Refinery IOCL	3,361.00	3,361.00	08/2021	08/2021	09/2022	13
	<u>POWER</u>						
13	BRBCL-NABINAGAR TPP- JV (4X250 MW) NTPC	5,353.00	10,566.00	07/2012	06/2021	07/2021	1

List of projects reporting additional delayed Rs. 1000 Crore and above							(April 2021)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
14	EASTERN REGION STRENGTHENING SCHEME- XVIII Central Sector Projects PGCIL	3,500.00	3,994.00	07/2020	05/2021	06/2021	1
15	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P PGCIL	14,733.37	14,733.37	11/2019	04/2021	06/2021	2
16	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) PGCIL	1,394.52	1,394.52	05/2017	06/2021	09/2021	3
17	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL NTPC	1,885.13	1,885.13	12/2018	03/2021	07/2021	4
	<u>RAILWAYS</u>						
18	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR NFR	1,180.19	4,541.38	12/2008	04/2021	05/2021	1
19	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF SR	931.98	1,121.00	N.A.	04/2021	05/2021	1
20	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) WR	829.74	1,959.74	03/2020	12/2023	03/2024	3
21	KATNI - SINGRAULI DOUBLING PROJECT WCR	1,763.93	1,762.94	03/2020	03/2023	03/2024	12
22	HUBLI- CHIKJAJUR SWR	1,156.94	1,656.00	03/2020	11/2021	03/2023	16
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
23	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU NHAI	1,166.26	1,296.93	N.A.	07/2021	08/2021	1
24	DELHI AGRA APPROVED LENGTH 180.0 KM NHAI PPP (BOT)	1,928.22	3,182.34	04/2015	03/2021	06/2021	3
25	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS NHAI	1,016.92	1,071.00	N.A.	07/2021	01/2022	6
26	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 MoRTH	1,069.59	1,069.59	10/2019	12/2020	08/2021	8
	<u>TELECOMMUNICATIONS</u>						
27	NETWORK FOR SPECTRUM DOT	13,334.00	24,664.00	07/2015	06/2021	07/2021	1

TABLE-35

Sector wise analysis of projects Rs. 1000 Crore and above					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	67,120.00	693,05.00	80,348.00	59,554.96
CIVIL AVIATION	5	7,613.90	76,13.90	7,703.90	1,801.92
COAL	30	1,08,556.34	1,106,30.02	1,13,115.57	39,088.99
MINES	1	5,540.00	64,35.90	5,540.00	731.55
STEEL	5	24,006.86	304,21.86	30,121.86	22,714.13
PETROLEUM	57	2,64,239.96	2,818,00.41	2,71,220.92	99,560.18
POWER	46	2,81,387.51	3,428,97.91	3,53,015.51	2,48,558.26
HEALTH AND FAMILY WELFARE	4	6,160.00	61,60.00	6,531.00	912.62
RAILWAYS	161	3,94,274.15	4,621,28.90	6,24,000.70	2,15,183.64
ROAD TRANSPORT AND HIGHWAYS	156	2,36,631.03	2,364,60.39	2,52,551.93	1,77,994.41
SHIPPING AND PORTS	1	5,369.18	53,69.18	4,633.81	1,871.35
TELECOMMUNICATIONS	1	13,334.00	133,34.00	24,664.00	17,845.00
URBAN DEVELOPMENT	23	2,78,636.14	2,829,26.12	3,01,082.00	1,34,630.76
WATER RESOURCES	1	10,151.04	555,48.87	55,548.87	17,325.20
HOME AFFAIRS	1	1,219.21	12,19.21	2,000.00	906.04
DPIIT	2	17,352.09	173,52.09	18,990.30	11,472.42
Grand total	498	17,21,591.41	19,29,603.76	21,51,068.37	10,50,151.43


TABLE-36

State-Wise Position of Central Sector Projects costing Rs. 1000 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	22	1,00,790.37	1,48,161.40	47.00	7	41,080.27	96,339.76	1 - 180
2	ARUNACHAL PRADESH	5	13,732.92	32,928.36	139.78	1	6,285.33	19,992.43	155 - 155
3	ASSAM	6	27,224.48	29,692.21	9.06	4	4,630.48	7,098.21	2 - 48
4	BIHAR	27	87,426.57	1,21,814.59	39.33	7	29,343.85	54,798.38	15 - 141
5	GUJARAT	24	87,824.17	98,441.87	12.09	6	25,968.21	35,962.79	3 - 74
6	HARYANA	12	16,498.78	18,358.28	11.27	0	0.00	0.00	-
7	HIMACHAL PRADESH	8	17,307.75	27,192.18	57.11	1	3,919.59	9,897.59	154 - 154
8	JAMMU AND KASHMIR	14	37,748.07	63,675.32	68.69	1	2,500.00	27,949.00	241 - 241
9	KARNATAKA	17	53,661.87	62,706.98	16.86	2	27,562.08	32,351.12	36 - 64
10	KERALA	11	32,478.92	37,206.00	14.55	4	7,431.46	9,221.96	32 - 53
11	MADHYA PRADESH	23	61,740.86	74,374.58	20.46	7	8,906.63	15,736.63	12 - 73
12	MAHARASHTRA	49	1,39,827.20	1,66,198.89	18.86	12	41,761.00	64,004.30	8 - 216
13	MANIPUR	1	4,454.17	12,264.15	175.34	1	4,454.17	12,264.15	153 - 153
14	MEGHALAYA	1	906.46	4,083.02	350.44	0	0.00	0.00	-
15	MIZORAM	1	2,393.47	5,521.45	130.69	1	2,393.47	5,521.45	108 - 108
16	NAGALAND	3	7,896.52	12,481.00	58.06	1	2,326.52	6,911.00	117 - 117
17	ODISHA	37	1,04,138.78	1,12,178.14	7.72	10	25,065.60	32,446.13	15 - 204
18	PUNJAB	4	5,049.00	7,181.59	42.24	0	0.00	0.00	-
19	RAJASTHAN	15	31,995.25	38,670.71	20.86	1	12,320.00	17,079.00	75 - 75
20	SIKKIM	1	1,339.48	8,600.00	542.04	0	0.00	0.00	-
21	TAMIL NADU	27	99,664.04	1,17,838.13	18.24	6	10,455.67	20,503.84	27 - 145
22	UTTAR PRADESH	48	1,40,935.26	1,47,900.58	4.94	4	20,290.86	21,462.80	8 - 39
23	WEST BENGAL	25	47,280.10	65,048.81	37.58	6	16,254.80	24,199.79	63 - 324
24	DELHI	9	80,186.38	81,749.70	1.95	2	5,992.21	7,178.00	24 - 26
25	CHHATISGARH	18	77,851.94	88,489.77	13.66	5	24,001.00	33,261.43	21 - 74
26	JHARKHAND	16	56,545.31	60,442.40	6.89	1	14,366.58	15,389.42	40 - 40
27	UTTARAKHAND	6	26,039.84	37,071.69	42.37	3	21,686.06	32,443.84	3 - 126
28	TELANGANA	6	19,991.02	22,099.10	10.55	1	10,598.98	10,997.70	20 - 20
29	MULTI STATE	62	3,38,662.43	4,48,697.47	32.49	28	82,832.57	1,37,524.58	9 - 276
Total		498	17,21,591.41	21,51,068.37	24.95	122	4,52,427.39	7,50,535.30	


^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

Graphical Presentation of All Projects w.r.t. Original Schedule

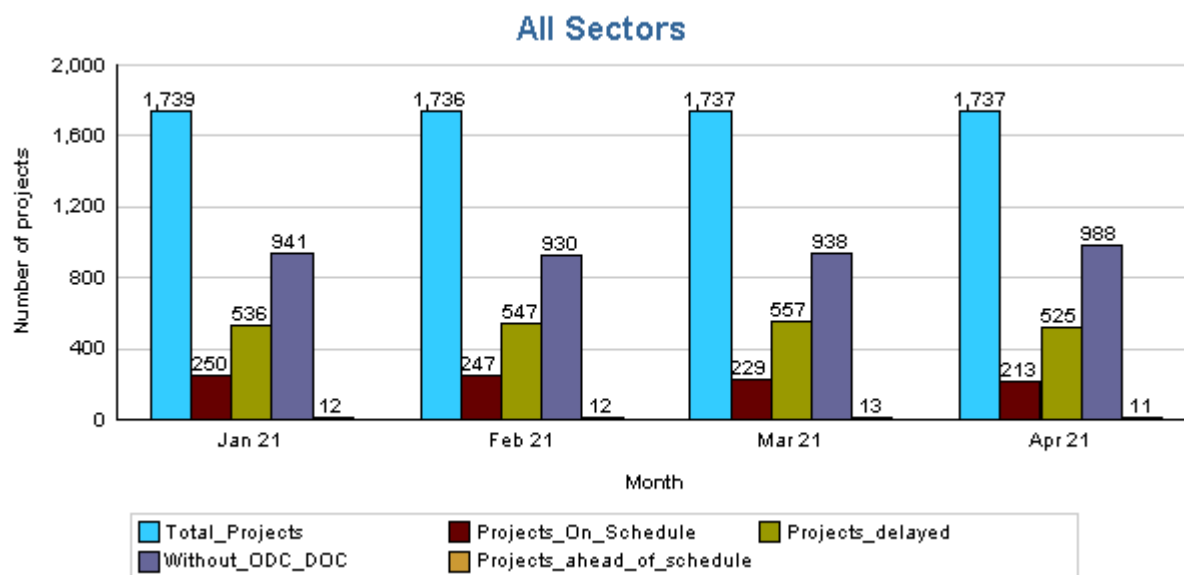

Break-up of 525 Delayed projects in April 2021

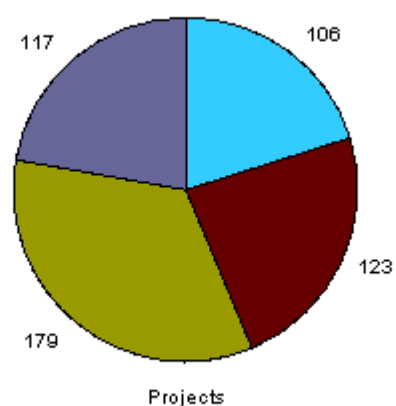


Delay in Months


Legend:

- 1-12 (Light Blue)
- 13-24 (Dark Red)
- 25-60 (Olive Green)
- MORE THAN 60 (Purple)

Graphical Presentation of HUMAN RESOURCE DEVELOPMENT Sector

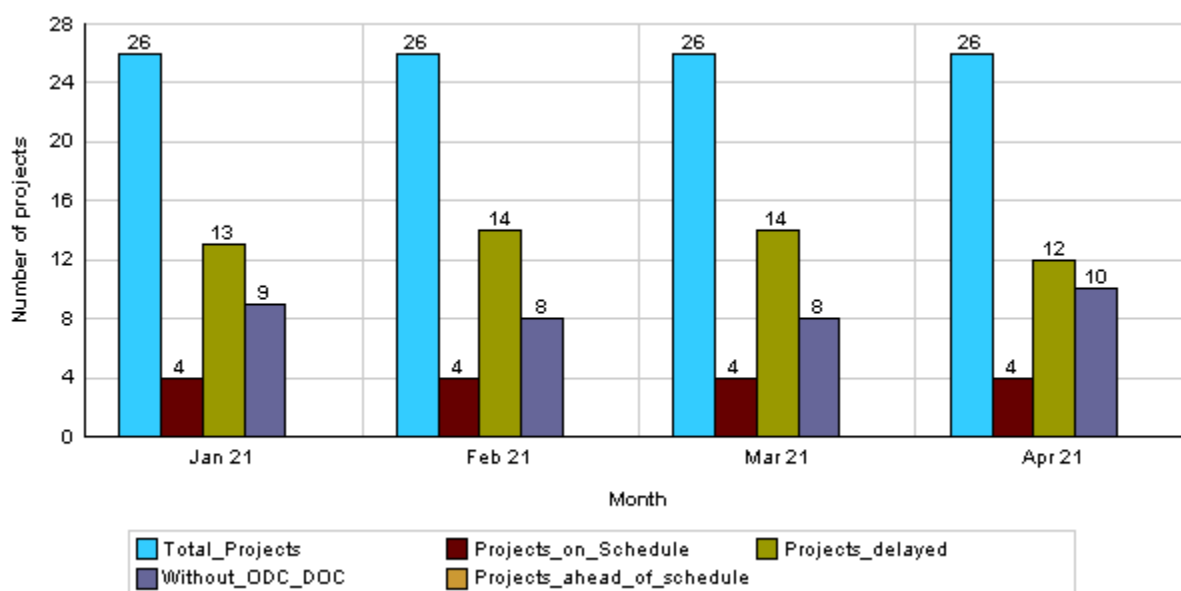


Break-up of 12 Delayed projects in April 2021

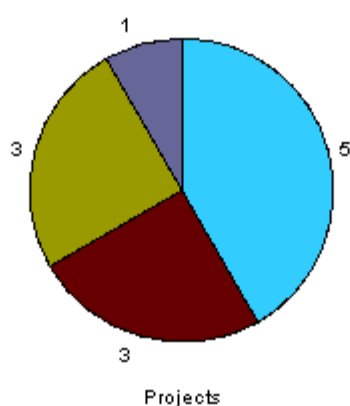

Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Projects	5	3	3	1

Graphical Presentation of HOME AFFAIRS Sector

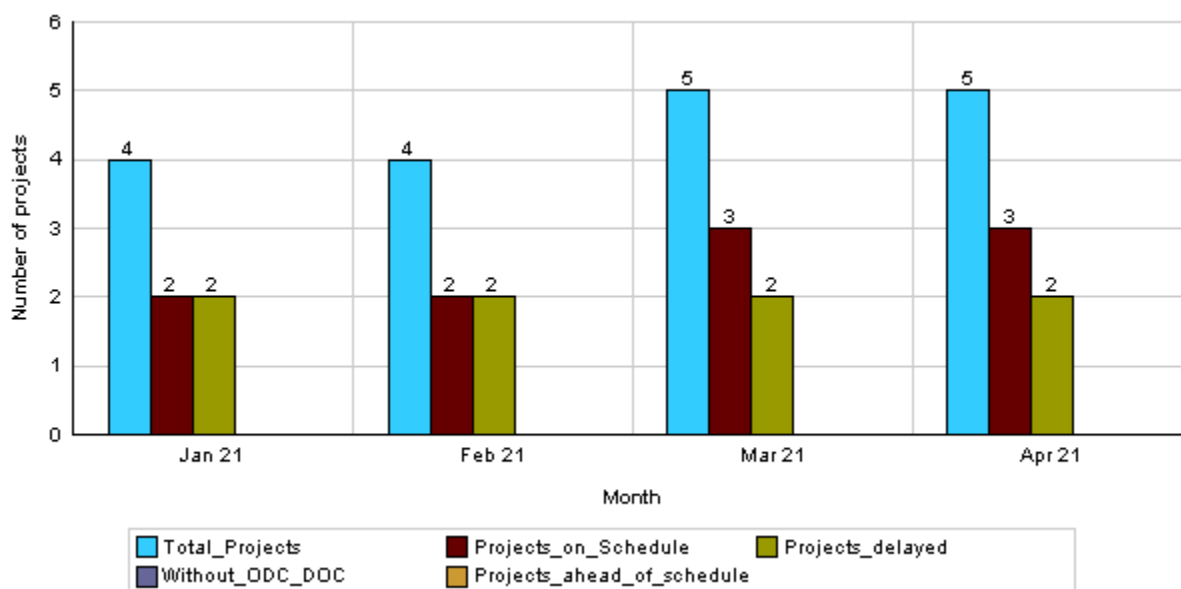


Break-up of 2 Delayed projects in April 2021




Delay in Months

1-12	13-24	25-60	MORE THAN 60
1	1	0	0

Graphical Presentation of HEALTH AND FAMILY WELFARE Sector

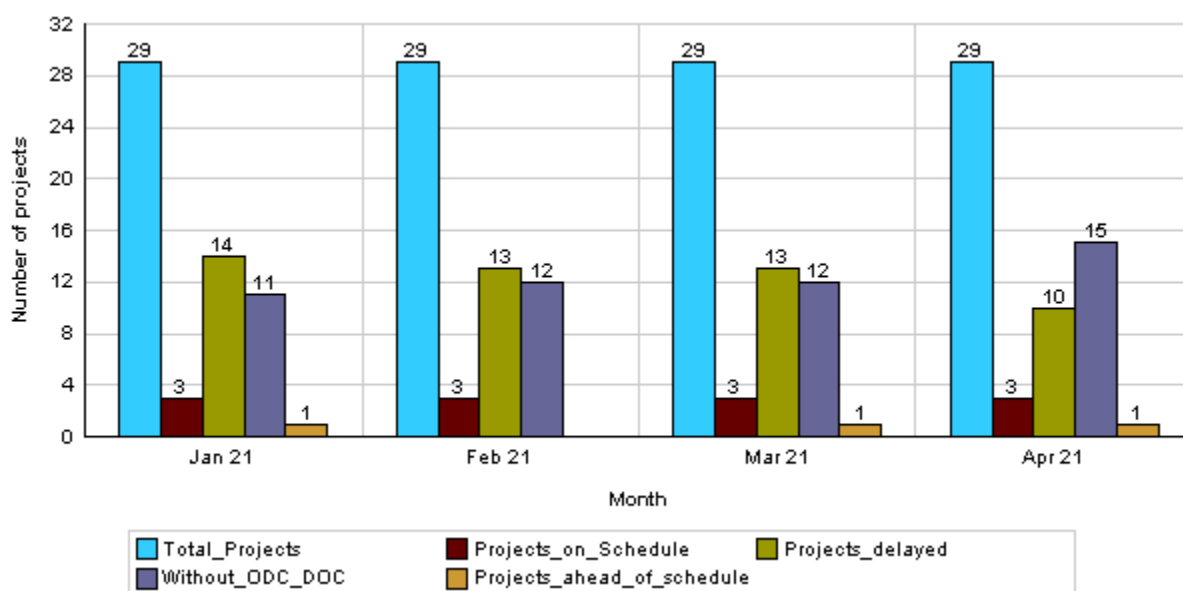


Break-up of 10 Delayed projects in April 2021

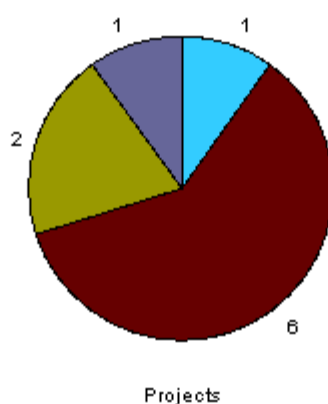


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of FERTILISERS Sector

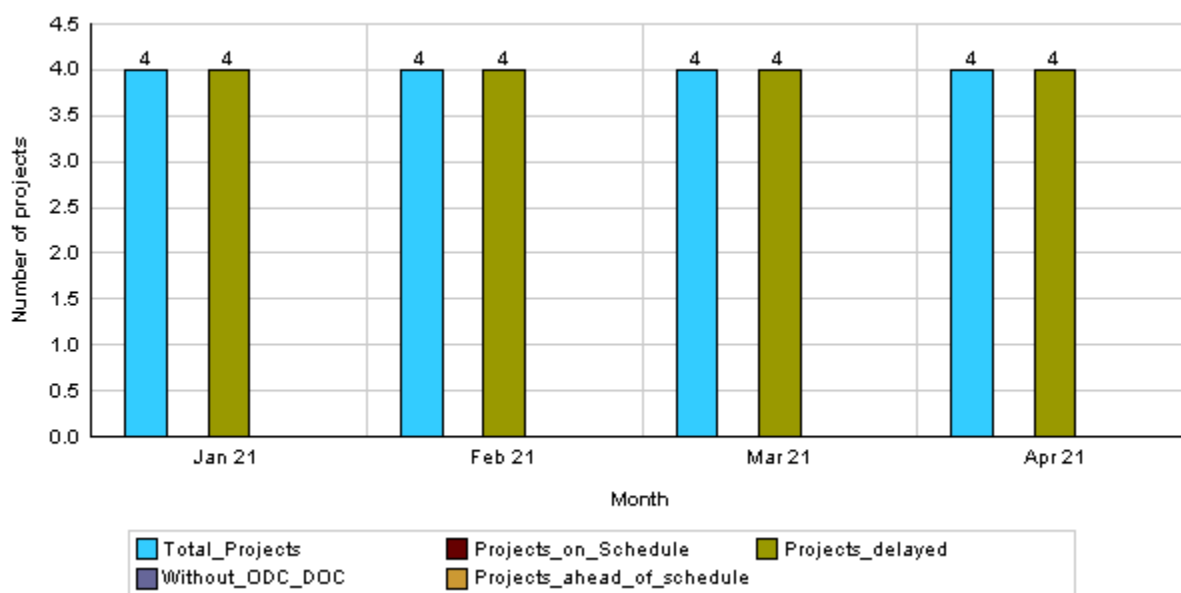


Break-up of 4 Delayed projects in April 2021

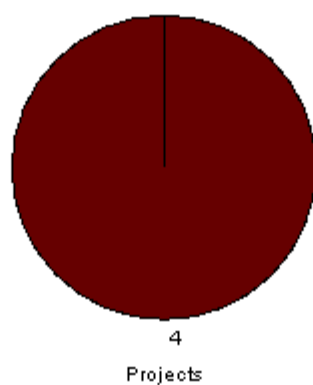


Delay in Months

Delay in Months	Count
1-12	0
13-24	4
25-60	0
MORE THAN 60	0

Graphical Presentation of DPIIT Sector

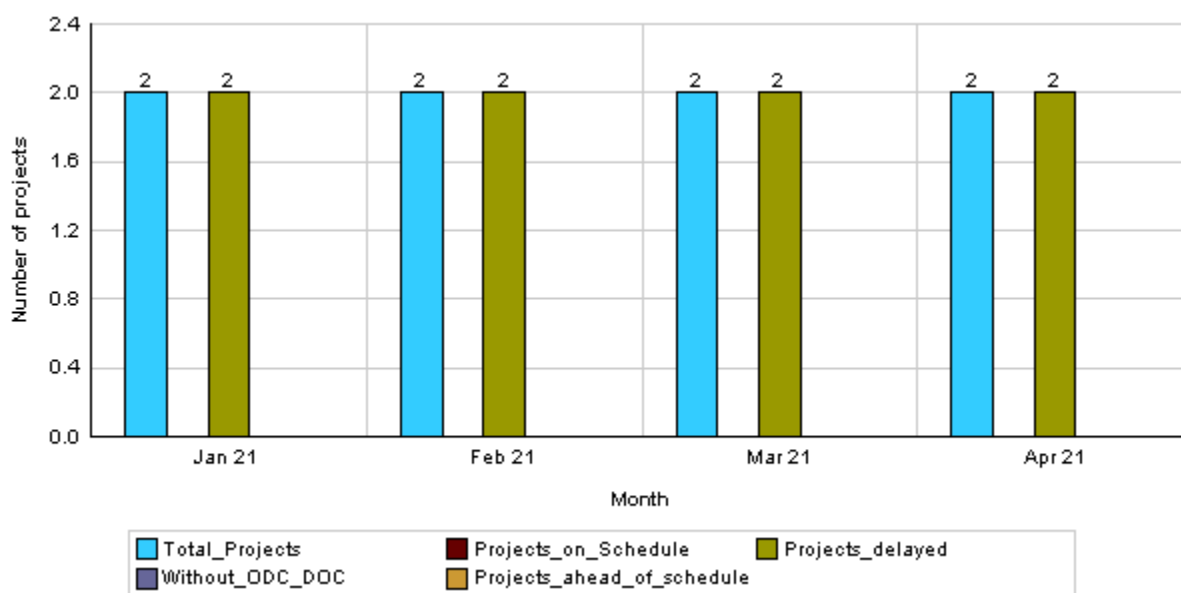


Break-up of 2 Delayed projects in April 2021

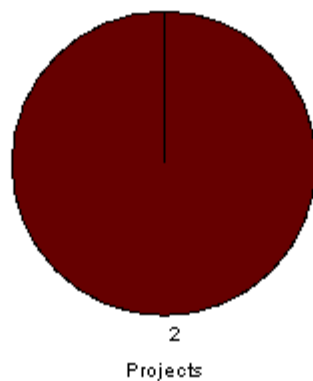


Delay in Months

Delay in Months	Count
1-12	0
13-24	2
25-60	0
MORE THAN 60	0

Graphical Presentation of RURAL DEVELOPMENT Sector

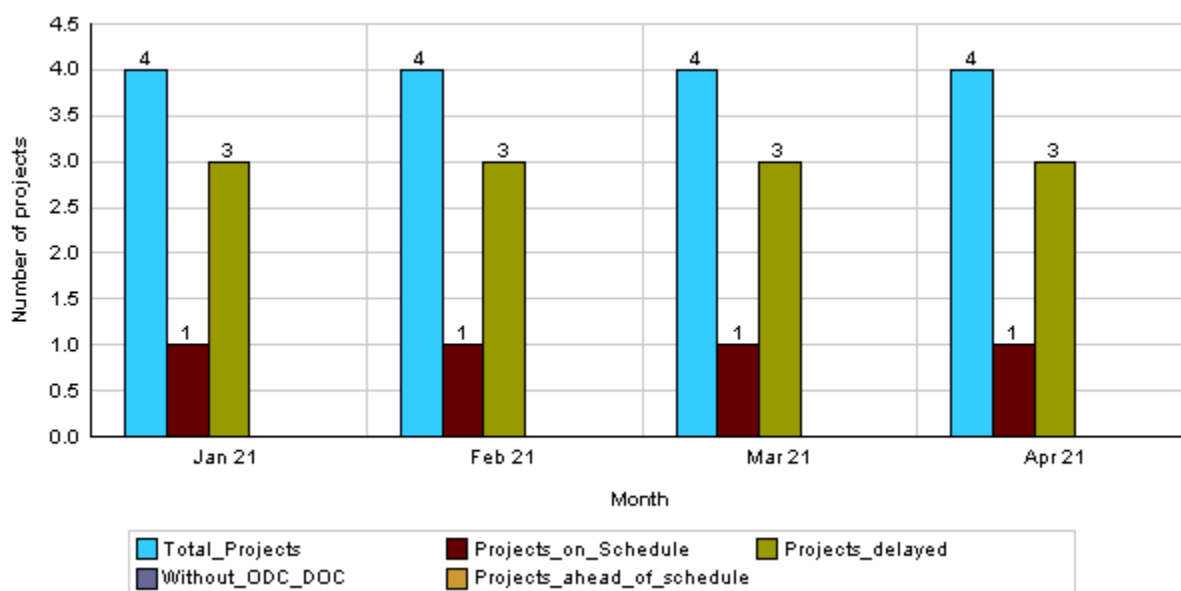


Break-up of 3 Delayed projects in April 2021

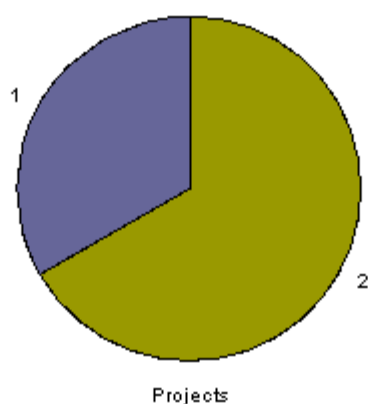


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	0	0	2	1

Graphical Presentation of HUMAN RESOURCE DEVELOPMENT Sector

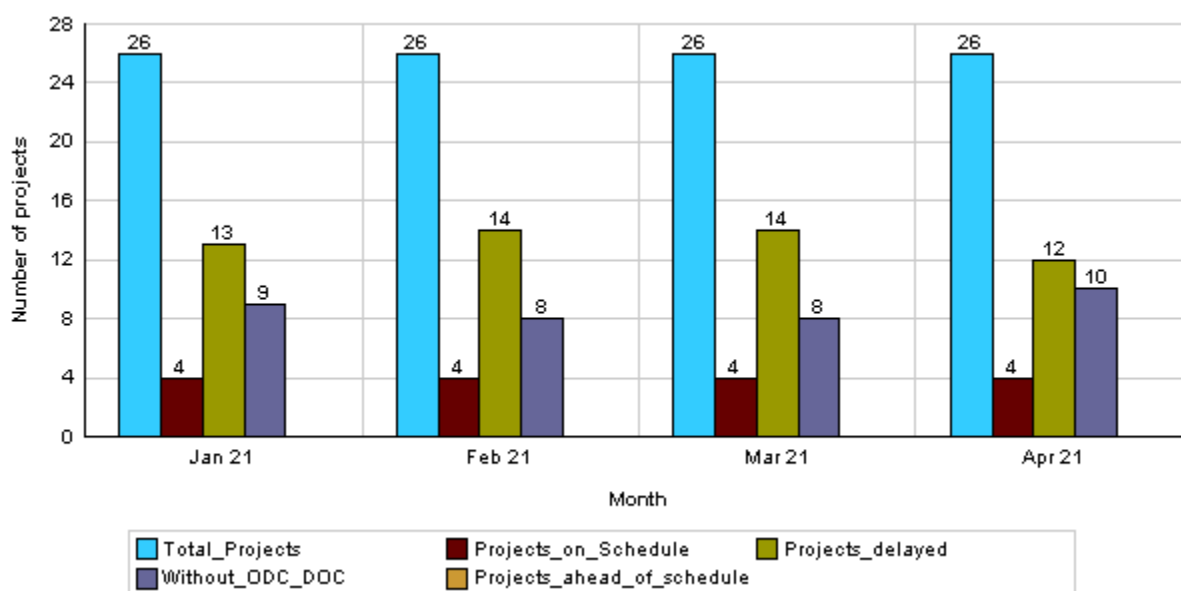


Break-up of 12 Delayed projects in April 2021

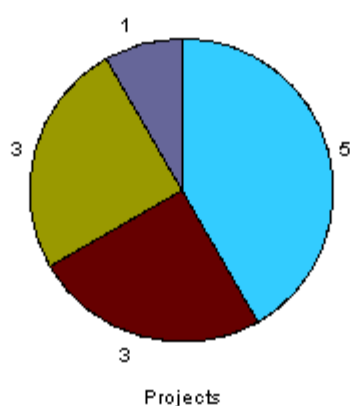


Delay in Months

1-12	13-24	25-60	MORE THAN 60
------	-------	-------	--------------

Graphical Presentation of WATER RESOURCES Sector

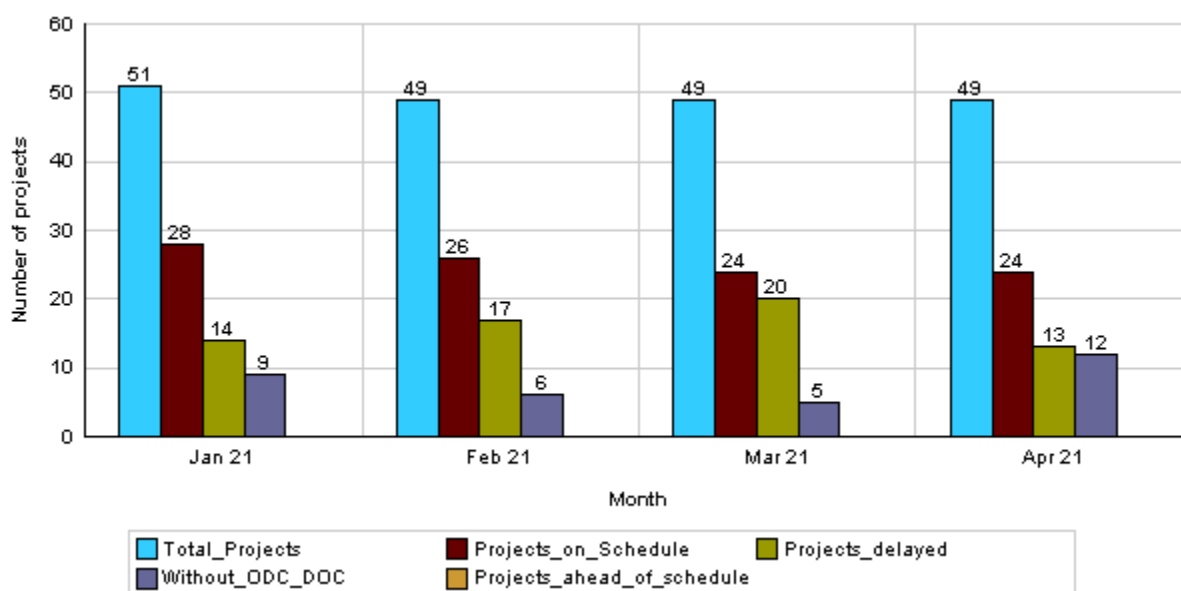


Break-up of 13 Delayed projects in April 2021

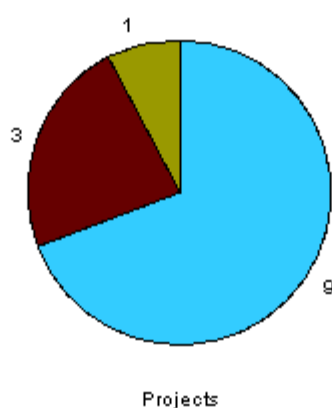

Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of TELECOMMUNICATIONS Sector

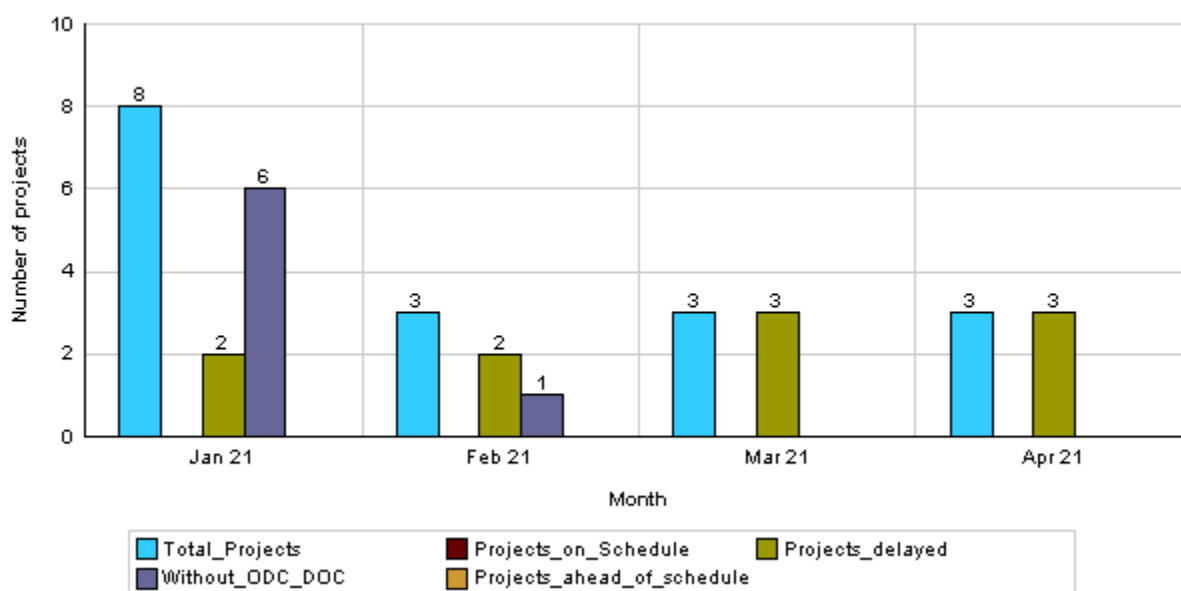


Break-up of 3 Delayed projects in April 2021




Delay in Months

1-12 13-24 25-60 MORE THAN 60

Graphical Presentation of ROAD TRANSPORT AND HIGHWAYS Sector

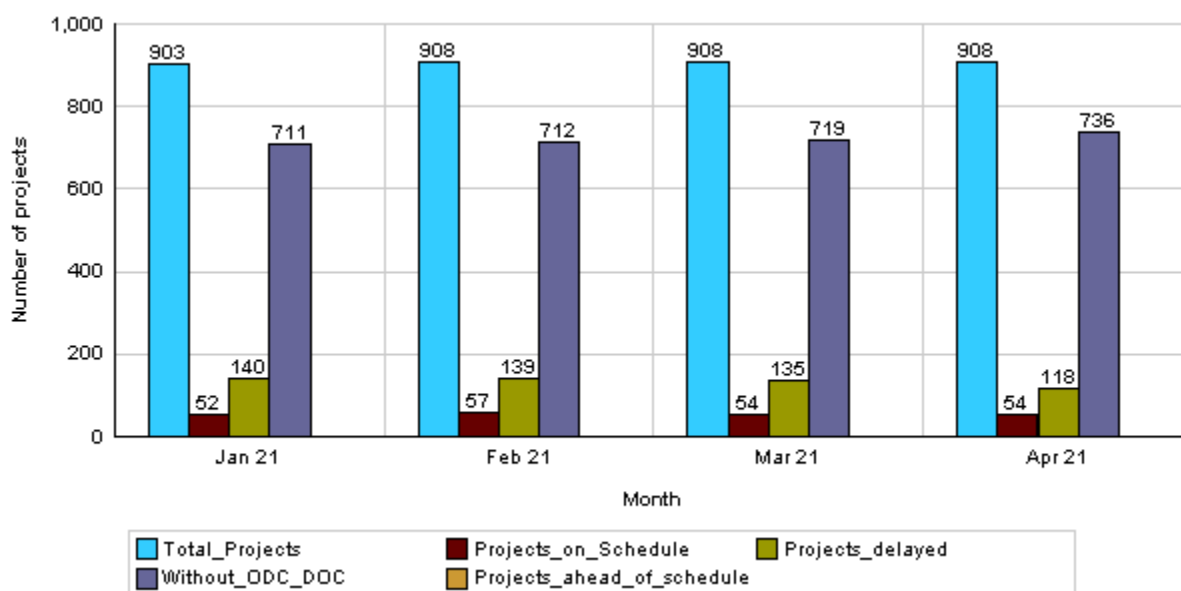


Break-up of 118 Delayed projects in April 2021

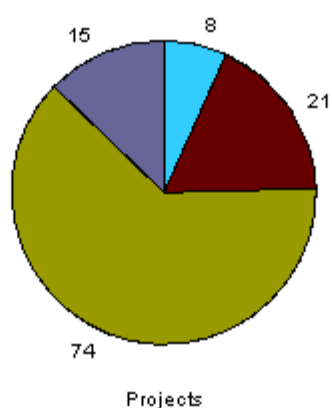


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of RAILWAYS Sector

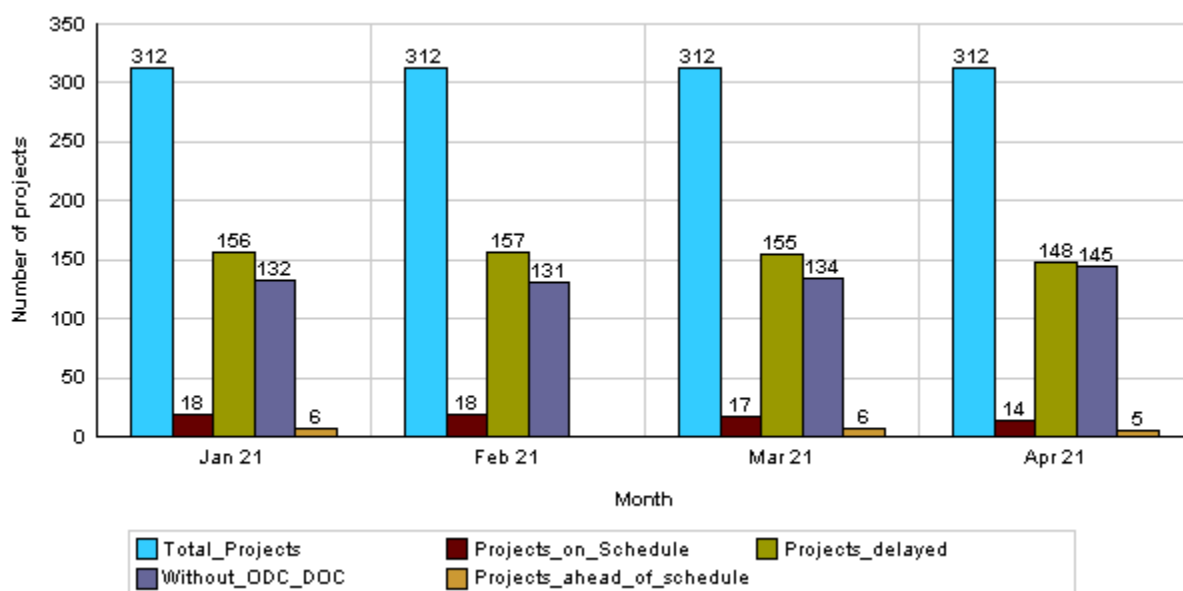


Break-up of 148 Delayed projects in April 2021

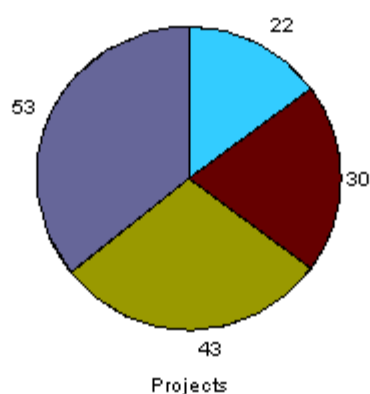


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of POWER Sector

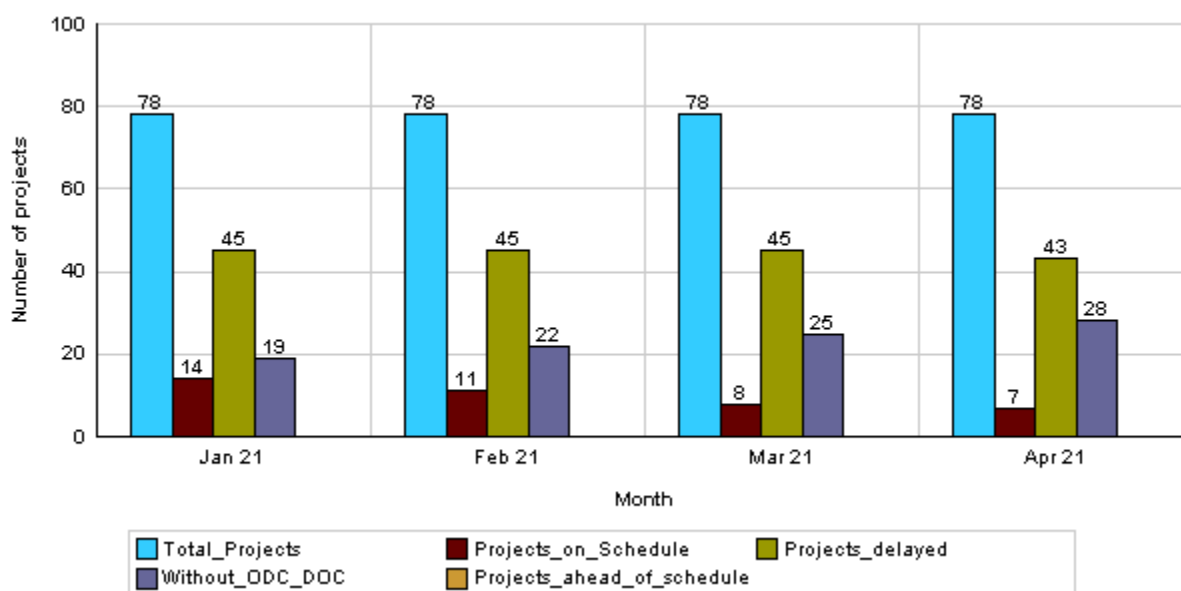


Break-up of 43 Delayed projects in April 2021

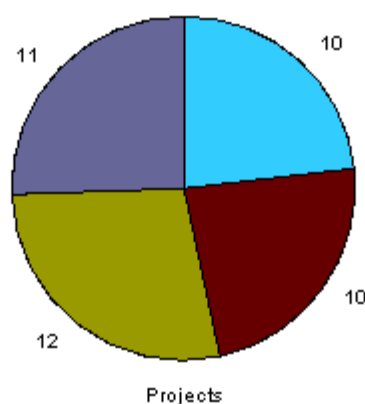


Delay in Months

1-12	13-24	25-60	MORE THAN 60
------	-------	-------	--------------

Graphical Presentation of PETROLEUM Sector

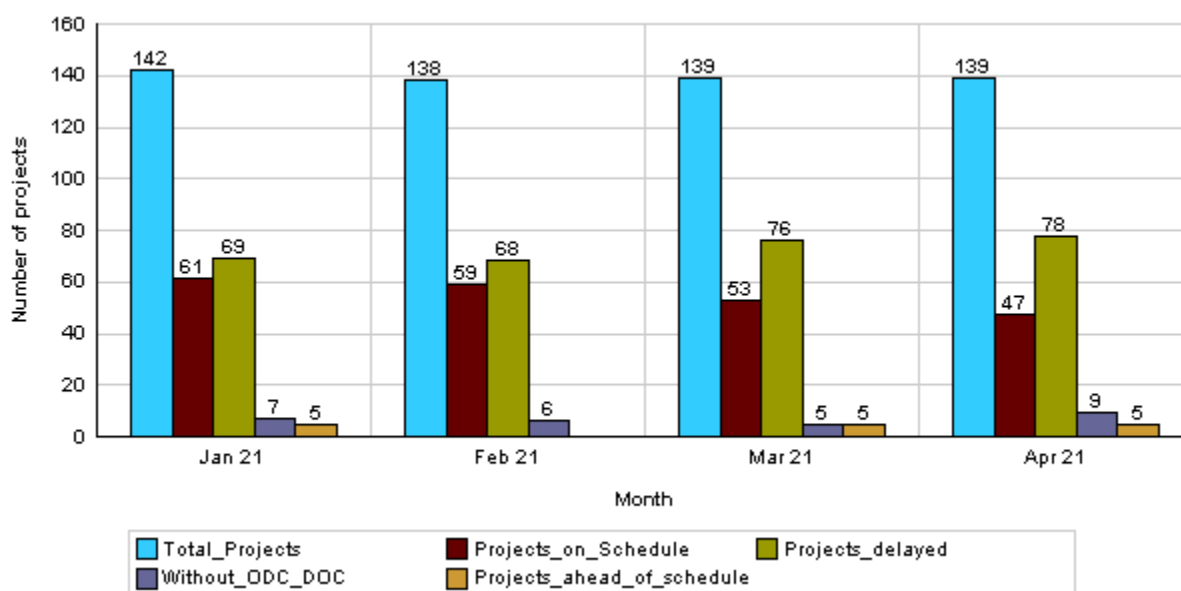


Break-up of 78 Delayed projects in April 2021

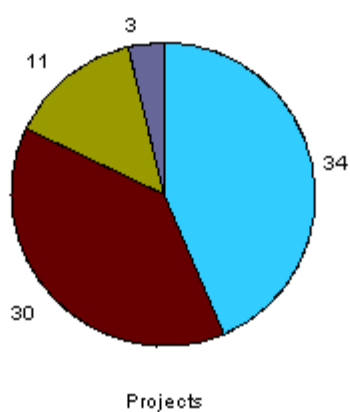


Delay in Months: 1-12, 13-24, 25-60, MORE THAN 60

Graphical Presentation of STEEL Sector

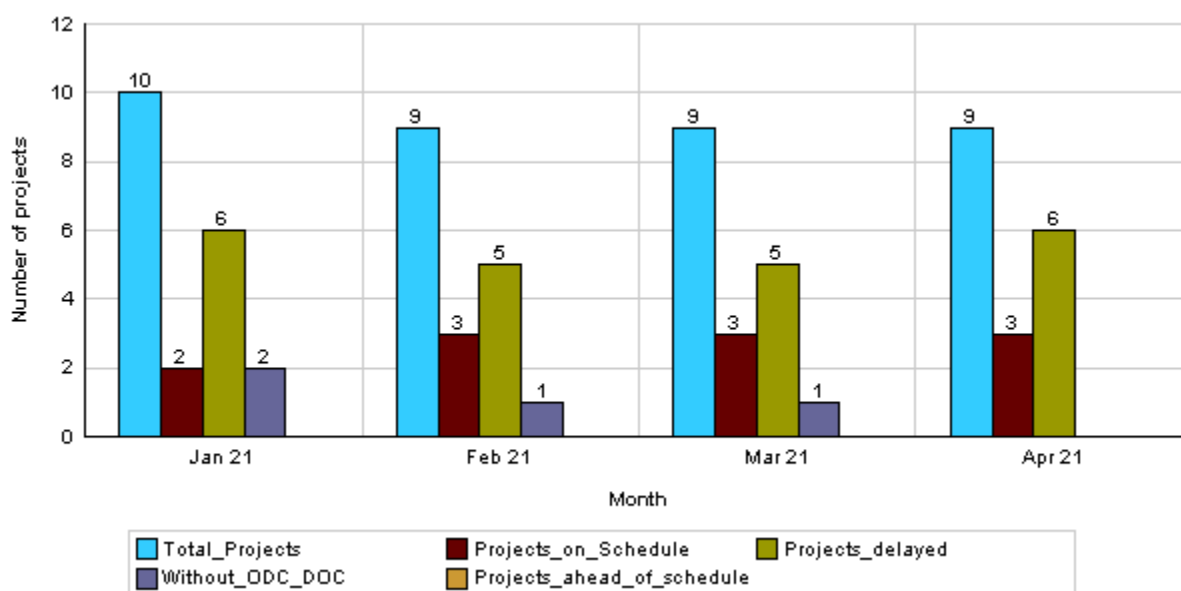


Break-up of 6 Delayed projects in April 2021

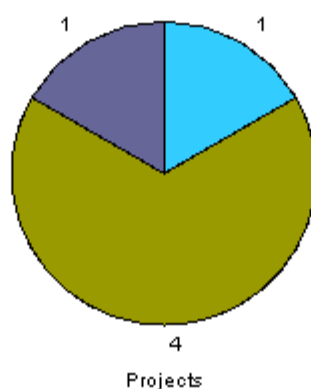


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of MINES Sector

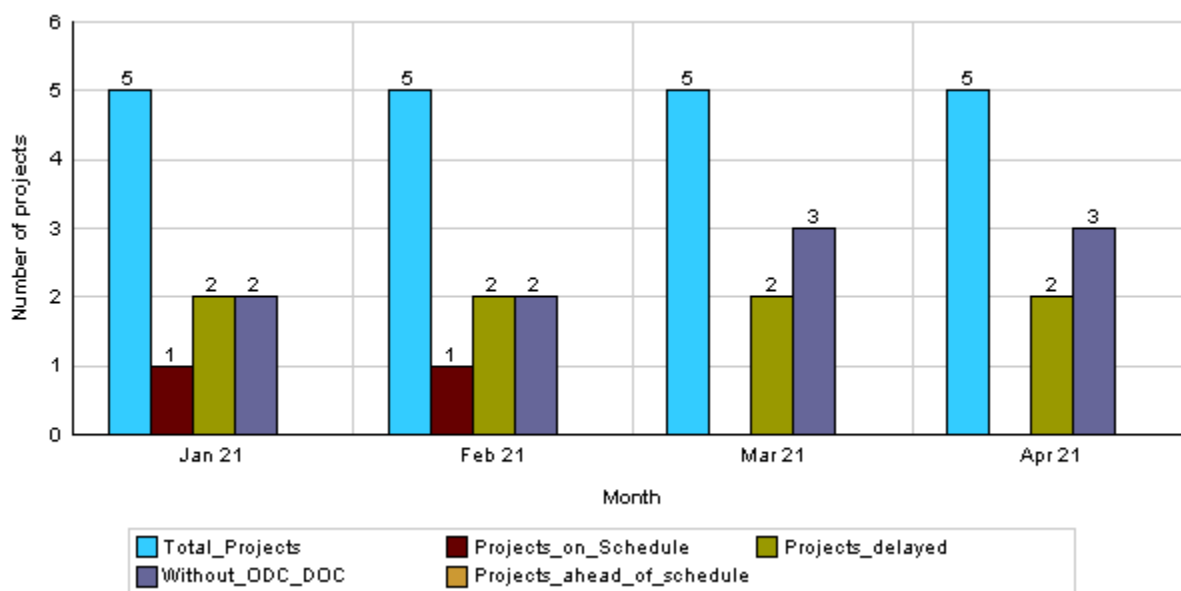


Break-up of 2 Delayed projects in April 2021




Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Count	0	2	0	0

Graphical Presentation of COAL Sector

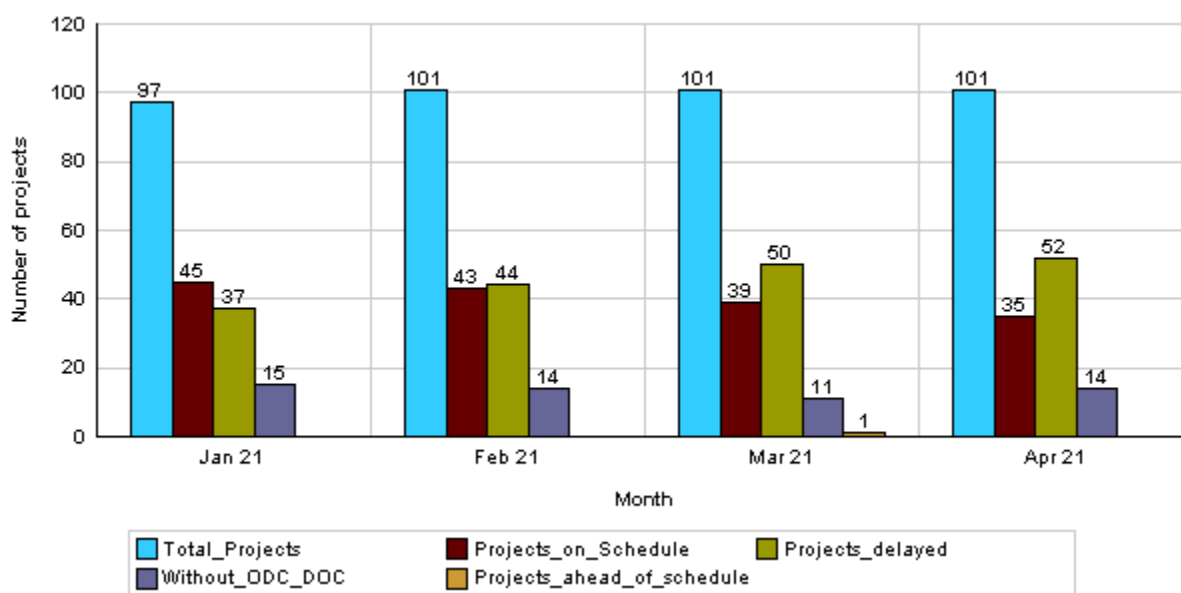


Break-up of 52 Delayed projects in April 2021

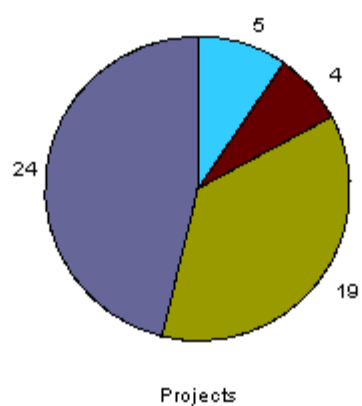


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	5	4	19	24

Graphical Presentation of CIVIL AVIATION Sector

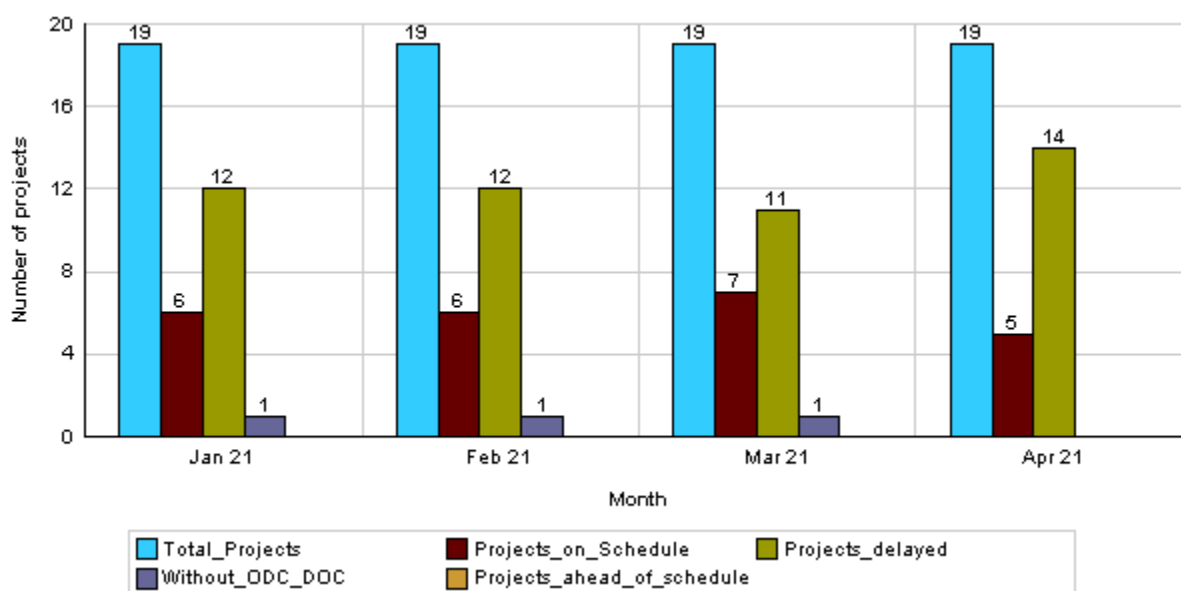


Break-up of 14 Delayed projects in April 2021

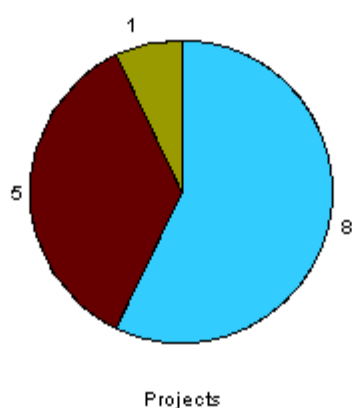


Delay in Months

1-12	13-24	25-60	MORE THAN 60

Graphical Presentation of URBAN DEVELOPMENT Sector

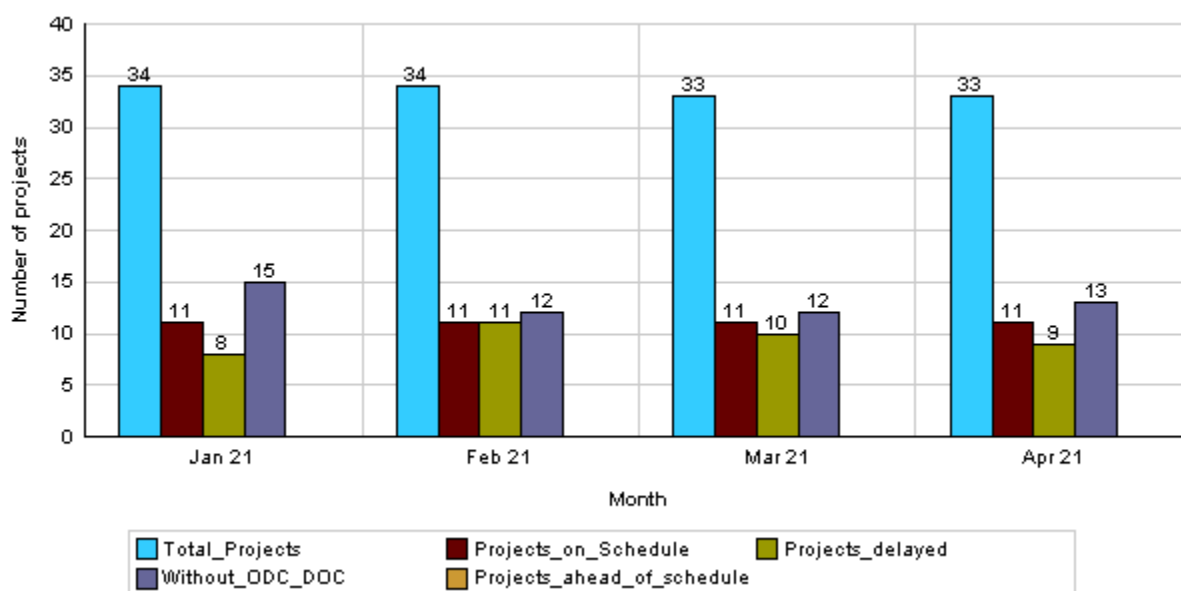


Break-up of 9 Delayed projects in April 2021

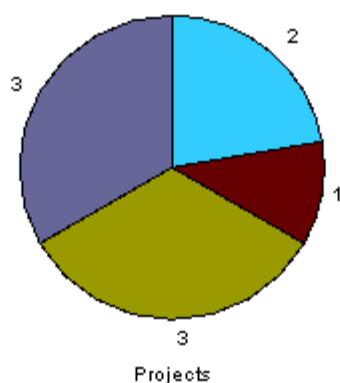


Delay in Months: 1-12 (Light Blue), 13-24 (Dark Red), 25-60 (Olive Green), MORE THAN 60 (Purple)

Graphical Presentation of ATOMIC ENERGY Sector

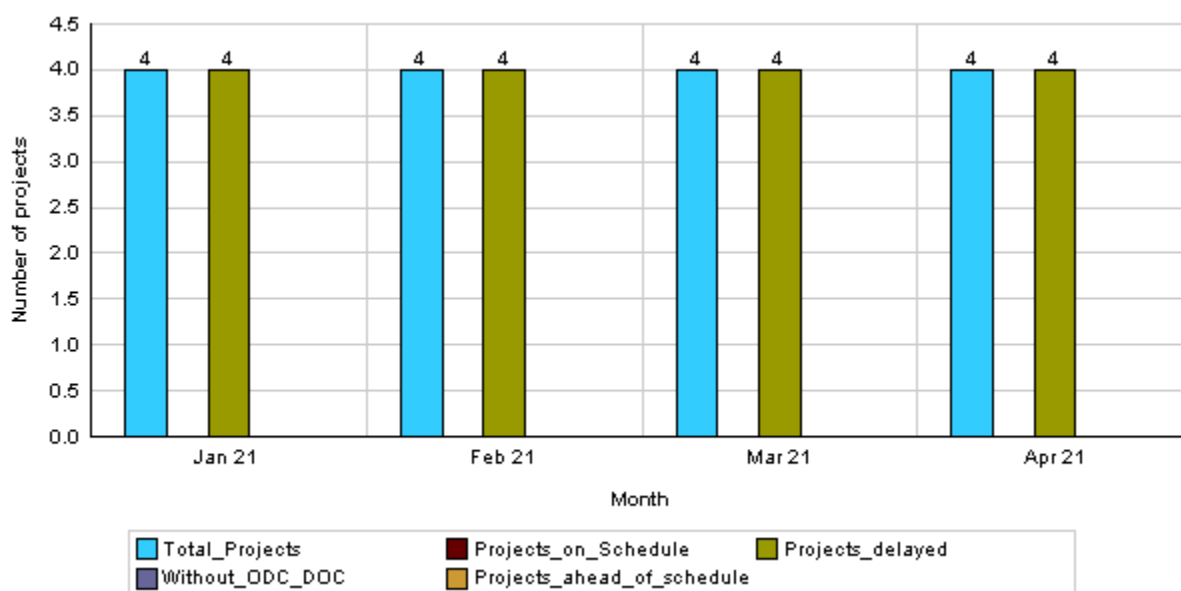

Break-up of 4 Delayed projects in April 2021

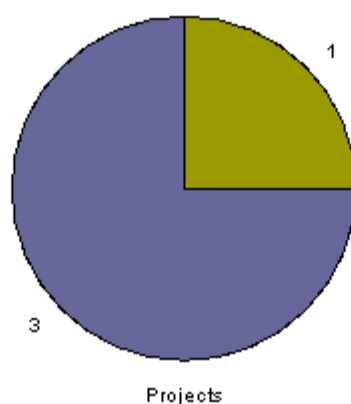

Delay in Months

Delay in Months	Count
1-12	0
13-24	0
25-60	1
MORE THAN 60	3

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT ,	10/2009	11,459.00 -	16,580.00	16,488.00	12/2015 -	02/2022	74(O) -	58/70
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN ,	10/2009	12,320.00 -	17,079.00	13,206.00	12/2016 -	03/2023	75(O) -	45/68
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI 500 MWE) - [020100044]BHAVNI,TAMIL NADU ,	09/2003	3,492.00 5,677.00	6,840.00	5,935.96	09/2010 09/2016	10/2022	145(O) 0	83/87
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL,TAMIL NADU , Central Sector Projects	03/2013	39,849.00 -	39,849.00	23,925.00	11/2020 -	11/2023	36(O) -	28/76
	Total		67,120.00 -	80,348.00	59,554.96				214/301
	<u>CIVIL AVIATION</u>								
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT PORTBLAIR - [N04000073]AAI,A & N ISLANDS ,	10/2013	417.23 707.73	707.73	379.95	09/2018 09/2020	06/2021	33(O) 0	0/6
6	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT - [N04000089]AAI,ANDHRA PRADESH ,	08/2017	177.10 -	177.10	86.01	02/2020 06/2021	12/2021	22(O) 6	1/4
7	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT - [N04000091]AAI,ANDHRA PRADESH ,	04/2020	611.80 -	611.80	21.25	03/2023 -	03/2023	0(O) -	3/14
8	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]AAI,ASSAM ,	12/2016	1,142.00 -	1,232.00	368.37	03/2021 03/2022	03/2022	12(O) -12	0/0
9	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES PHASE I AND II - [N04000082]AAI,BIHAR ,	05/2018	1,216.90 -	1,216.90	205.04	10/2022 -	03/2023	5(O) -	0/3
10	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA BCAS AAIB AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076]AAI,DELHI ,	11/2016	303.80 351.21	303.80	167.55	04/2020 -	03/2022	23(O) -	0/0
11	C/O NEW GREENFIELD AIRPORT AT HISSAR RAJKOT GUJARAT - [N04000088]AAI,GUJARAT ,	01/2018	1,405.00 -	1,405.00	250.63	08/2022 -	08/2022	0(O) -	0/15
12	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]AAI,JAMMU AND KASHMIR ,	07/2018	346.27 -	480.33	51.11	09/2021 -	09/2021	0(O) -	0/4
13	UPGRADATION OF JABALPUR AIRPORT - [N04000087]AAI,MADHYA PRADESH ,	06/2016	412.24 -	412.24	195.70	06/2021 -	12/2021	6(O) -	0/1
14	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING RECONSTRUCTION OF OLD TERMINAL BUILDING MODIFICAT - [N04000079]AAI,MAHARASHTRA ,	03/2017	475.39 -	475.39	88.11	04/2021 -	04/2021	0(O) -	0/1
15	MODERNIZATION OF CHENNAI AIRPORT PHASE II CHENNAI - [N04000074]AAI,TAMIL NADU ,	06/2018	2,467.00 -	2,467.00	608.22	02/2022 -	08/2022	6(O) -	0/12

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
16	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]AAI,TAMIL NADU ,	08/2018	951.28 -	951.28	408.94	10/2021 -	07/2022	9(O) -	0/13
17	DEVELOPMENT OF TUTICORIN AIRPORT - [N04000090]AAI,TAMIL NADU ,	06/2019	380.87 -	380.87	5.99	03/2022 03/2022	03/2023	12(O) 0	0/14
18	CO CIVIL AVIATION REASEARCH ORG. (PH-II) AT BEGUMPET AIRPORT HYDRABAD - [N04000086]AAI,TELANGANA ,	05/2020	353.61 -	353.61	61.13	05/2022 -	05/2022	0(O) -	0/4
19	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI,TRIPURA ,	09/2015	438.28 -	402.00	366.61	06/2019 12/2020	06/2021	24(O) -2	0/1
20	CCS INTERNATIONAL AIRPORT LUCKNOW - [N04000077]AAI,UTTAR PRADESH ,	06/2018	1,383.00 -	1,383.00	369.66	09/2021 -	09/2022	12(O) -	0/0
21	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT DEHRADUN - [N04000085]AAI,UTTARAKHAND ,	07/2018	456.86 -	456.86	286.85	09/2020 -	12/2021	15(O) -	0/1
22	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA - [N04000080]AAI,WEST BENGAL ,	01/2016	458.00 -	458.00	135.60	03/2020 12/2021	12/2021	21(O) 6	0/0
23	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT KOLKATA - [N04000081]AAI,WEST BENGAL ,	01/2019	389.71 -	389.71	140.62	11/2021 10/2022	10/2022	11(O) 0	0/2
	Total		13,786.34 -	14,264.62	4,197.34				4/95
	<u>COAL</u>								
24	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL,CHHATISGARH ,	06/2010	11,816.40 -	11,816.40	4,487.05	03/2023 03/2016	03/2023	0(O) 0	15/21
25	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH ,	08/2013	7,612.33 -	7,612.33	2,745.45	03/2023 -	03/2023	0(O) -	13/22
26	PELMA OCP(15.00MTY) - [N06000045]SECL,CHHATISGARH ,	11/2014	1,624.59 -	1,624.59	9.09	03/2023 -	03/2023	0(O) -	1/12
27	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH ,	09/2008	152.43 459.49	459.49	202.90	03/2015 03/2020	03/2022	84(O) 0	9/11
28	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH ,	07/2008	178.44 -	178.44	6.50	03/2014 -	03/2022	96(O) -	3/9
29	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH ,	12/2009	321.50 -	321.50	211.38	03/2014 -	03/2021	-	5/6
30	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH ,	12/2013	610.63 -	610.63	152.93	03/2022 -	03/2022	0(O) -	4/11
31	AMERA OC RCE - [N06000123]SECL,CHHATISGARH ,	02/2015	335.97 -	335.97	49.49	03/2018 -	03/2023	60(O) -	1/7
32	AMGAON OPENCAST PROJECT RCE - [N06000135]SECL,CHHATISGARH ,	07/2015	316.10 -	316.10	141.02	03/2020 -	03/2023	36(O) -	3/6
33	DURGAPUR OPENCAST PROJECT - [N06000136]SECL,CHHATISGARH ,	02/2015	916.24 -	916.24	11.38	03/2023 -	03/2026	36(O) -	2/12
34	MADANNAGAR OPENCAST PROJECT - [N06000140]SECL,CHHATISGARH ,	10/2015	1,875.32 -	1,875.32	.00	03/2024 -	03/2024	0(O) -	2/6
35	VIJAY WEST OPENCAST PROJECT - [N06000158]SECL,CHHATISGARH ,	05/2017	976.95 -	976.95	75.96	03/2026 -	03/2026	0(O) -	2/2

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
36	MAHAMAYA OPENCAST PROJECT - [N06000164]SECL,CHHATISGARH ,	05/2018	410.26 -	410.26	28.26	03/2026 -	03/2026	0(O) -	2/4
37	JHIRIA WEST OPENCAST PROJECT - [N06000166]SECL,CHHATISGARH ,	11/2018	389.97 -	389.97	.00	03/2026 -	03/2026	0(O) -	3/5
38	BAROUD OC EXPANSION (3-10 MTY) - [N06000197]SECL,CHHATISGARH ,	08/2020	2,309.80 -	2,309.80	275.61	03/2029 -	03/2029	0(O) -	0/0
39	JAMPALI OCP RCE - [N06000198]SECL,CHHATISGARH ,	05/2020	278.64 -	278.64	183.02	03/2024 -	03/2024	0(O) -	0/0
40	PORDA CHIMTAPANI OCP (10 MTY) - [N06000199]SECL,CHHATISGARH ,	12/2020	2,310.12 -	2,310.12	.00	03/2029 -	03/2029	0(O) -	0/0
41	DIPKA OC EXPANSION 40 MTY - [N06000200]SECL,CHHATISGARH ,	12/2020	5,241.40 -	5,241.40	1,931.58	03/2029 -	03/2029	0(O) -	0/0
42	MAGADH EXPANSION OC(51 MTY) - [N06000015]CCL,JHARKHAND ,	08/2008	6,964.33 6,964.33	706.40	706.20	07/2012 03/2025	03/2025	152(O) 0	7/7
43	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND ,	08/2007	163.51 -	163.51	107.27	03/2011 -	03/2022	132(O) -	7/7
44	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND ,	12/2009	510.85 -	510.85	426.30	03/2016 -	03/2022	72(O) -	7/7
45	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND ,	06/2009	162.46 -	162.46	98.21	03/2014 -	03/2022	96(O) -	7/7
46	MURAIIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND ,	02/2011	339.88 -	339.88	24.23	04/2014 -	04/2023	108(O) -	4/7
47	MOONIDH XV SEAM UG - [N06000098]BCCL,JHARKHAND ,	08/2011	1,230.27 -	1,230.27	463.92	04/2015 -	03/2022	83(O) -	2/6
48	RECAST EPR AMRAPALI OC - [N06000103]CCL,JHARKHAND ,	02/2012	4,983.58 4,983.58	4,983.58	245.85	03/2020 03/2024	03/2024	48(O) 0	8/8
49	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND ,	02/2014	555.52 -	555.52	5.87	03/2021 -	-	-	0/2
50	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND ,	08/2010	289.45 -	289.45	281.33	05/2014 -	07/2021	86(O) -	0/8
51	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND ,	10/2012	269.82 -	269.82	208.76	04/2014 -	04/2020	-	0/10
52	HURA - C OC (3 MTY) - [N06000143]ECL,JHARKHAND ,	10/2015	359.69 -	359.69	247.51	03/2022 -	03/2022	0(O) -	4/22
53	CHITRA EAST (RCE) OCP - [N06000169]ECL,JHARKHAND ,	08/2018	513.98 -	513.98	121.23	03/2024 -	03/2024	0(O) -	0/17
54	NORTH URIMARI EXPANSION OCP - [N06000182]CCL,JHARKHAND ,	03/2019	1,553.06 -	1,553.06	277.47	03/2023 -	03/2023	0(O) -	2/2
55	TETARIAKHAR EXPANSION OCP - [N06000186]CCL,JHARKHAND , Central Sector Projects	11/2019	243.52 -	243.52	39.79	03/2023 -	03/2023	0(O) -	1/1
56	PACHWARA SOUTH COAL BLOCK - [N06000193]NLC,JHARKHAND ,	07/2013	1,795.01 -	1,795.01	34.88	08/2022 -	09/2023	13(O) -	5/11
57	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]BCCL,JHARKHAND ,	10/2015	243.00 334.27	334.27	18.35	04/2018 -	06/2022	50(O) -	0/0
58	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH ,	02/2015	481.60 -	481.60	.00	03/2023 -	03/2023	0(O) -	3/10
59	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH ,	12/2014	357.80 -	357.80	100.63	03/2021 04/2024	04/2024	37(O) 0	4/10
60	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH ,	12/2014	371.04 -	371.04	77.27	03/2021 -	03/2024	36(O) -	5/9
61	BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH ,	07/2015	231.92 -	231.92	1.62	03/2022 -	03/2022	0(O) -	1/10

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
62	AMADAND OPENCASST EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH ,	03/2016	869.44 -	869.44	123.17	03/2021 -	03/2022	12(O) -	4/6
63	RPR FOR JAMUNIA UG (0.90 MTY) - [N06000153]WCL,MADHYA PRADESH ,	07/2016	281.25 -	281.25	21.35	03/2022 -	03/2026	48(O) -	0/0
64	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL,MADHYA PRADESH , Central Sector Projects	05/2017	1,783.09 -	1,783.09	622.66	03/2021 -	03/2022	12(O) -	3/9
65	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]NCL,MADHYA PRADESH ,	11/2017	1,255.17 -	1,255.17	152.16	03/2022 -	03/2023	12(O) -	3/9
66	SEMARIA OPENCASST PROJECT - [N06000176]NCL,MADHYA PRADESH ,	05/2019	396.58 -	396.58	.00	03/2026 -	03/2026	0(O) -	1/5
67	VISHNUPURI UG TO OC MINE - [N06000178]WCL,MADHYA PRADESH ,	07/2018	195.57 -	195.57	2.94	03/2025 -	03/2025	0(O) -	0/7
68	GANDHIGRAM UG MINE - [N06000183]WCL,MADHYA PRADESH ,	08/2019	414.16 -	414.16	.87	03/2026 -	03/2026	0(O) -	0/7
69	BLOCK-B EXPANSION OPENCASST PROJECT - [N06000184]NCL,MADHYA PRADESH ,	07/2019	998.71 -	998.71	.00	03/2023 -	03/2023	0(O) -	1/7
70	NIGAH EXPANSION OCP (15 TO 25 MTPA) - [N06000196]NCL,MADHYA PRADESH ,	11/2020	1,729.68 -	1,729.68	.00	03/2025 -	03/2025	0(O) -	0/8
71	PR FOR DINESH(MAKARDHOKRA III) EXPANSION OC (8.0 MTY) - [N06000118]WCL,MAHARASHTRA ,	11/2014	1,184.33 -	1,184.33	383.13	03/2020 -	03/2027	84(O) -	5/8
72	BHANEAGAON OC - [N06000121]WCL,MAHARASHTRA ,	02/2015	187.94 -	409.68	86.81	03/2023 -	03/2023	0(O) -	7/11
73	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA ,	05/2015	295.56 -	496.38	164.25	03/2019 -	09/2026	90(O) -	10/13
74	SINGHORI OC MINE - [N06000130]WCL,MAHARASHTRA ,	06/2015	205.49 -	205.49	138.12	03/2020 -	09/2021	18(O) -	7/10
75	AMALGAMATED PAUNI-II OC MINE - [N06000131]WCL,MAHARASHTRA ,	06/2015	483.69 499.00	499.00	252.15	03/2021 -	03/2021	-	3/6
76	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]WCL,MAHARASHTRA ,	08/2015	727.28 745.03	745.03	365.38	03/2025 -	03/2025	0(O) -	7/13
77	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA ,	08/2015	288.90 -	333.43	142.27	03/2023 -	03/2024	12(O) -	3/10
78	REVISED PR FOR AMALGAMATED INDER KAMPTEE DEEP OC (3.2 MTY) - [N06000141]WCL,MAHARASHTRA ,	11/2015	313.34 -	313.34	148.72	03/2021 -	03/2024	36(O) -	5/6
79	RPR FOR MUNGOLI NIORGUDA EXTENSION (DEEP) OC (4.375 MTY) - [N06000142]WCL,MAHARASHTRA ,	11/2015	851.60 -	826.80	230.50	03/2020 -	03/2026	72(O) -	2/6
80	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL,MAHARASHTRA ,	02/2016	198.68 -	325.18	253.17	03/2019 -	03/2022	36(O) -	4/9
81	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA ,	02/2016	304.52 -	729.86	160.67	03/2019 -	09/2026	90(O) -	5/8
82	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL,MAHARASHTRA ,	03/2017	362.73 -	402.90	330.34	03/2020 -	09/2022	30(O) -	0/0
83	UKNI DEEP OC - [N06000179]WCL,MAHARASHTRA ,	11/2018	318.14 -	318.14	211.41	03/2021 -	09/2022	18(O) -	0/4
84	BELLORA-NAIGAON DEEP OC - [N06000180]WCL,MAHARASHTRA ,	11/2018	252.71 -	252.71	101.09	03/2021 -	09/2022	18(O) -	0/3
85	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]WCL,MULTI STATE ,	08/2016	319.76 -	404.45	246.02	03/2022 -	03/2022	0(O) -	0/3
86	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]WCL,MULTI STATE ,	09/2016	289.29 -	289.30	35.95	03/2022 -	03/2025	36(O) -	2/12

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
87	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL,MULTI STATE ,	02/2017	328.00 -	328.00	295.83	03/2021 -	09/2023	30(O) -	3/6
88	BINA KAKRI AMALGAMATION OCP 14 MTPA - [N06000192]NCL,MULTI STATE ,	08/2020	836.42 -	836.42	60.07	03/2024 -	03/2024	0(O) -	0/6
89	BHUBANESWARI EXPENSION OCP(40.0 MTY) - [N06000034]MCL,ODISHA ,	12/2007	3,145.45 -	3,145.45	612.55	03/2017 -	03/2031	168(O) -	11/12
90	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY) - [N06000035]MCL,ODISHA ,	12/2007	8,416.19 8,416.19	8,416.19	890.78	03/2013 03/2028	03/2028	180(O) 0	8/10
91	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY) - [N06000044]MCL,ODISHA ,	12/2007	3,504.21 3,504.21	3,504.21	607.83	03/2010 03/2029	03/2029	228(O) 0	3/5
92	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA ,	08/2008	207.28 -	207.28	168.13	03/2012 -	03/2021	-	5/7
93	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA ,	11/2008	479.53 -	479.53	475.14	03/2013 -	03/2022	108(O) -	6/9
94	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA ,	05/2014	479.15 -	479.15	278.53	03/2019 -	03/2024	60(O) -	3/9
95	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA ,	05/2014	3,756.36 -	3,756.36	1,986.09	03/2026 -	03/2026	0(O) -	7/15
96	GARJANBAHAL OCP - [N06000117]MCL,ODISHA ,	11/2014	1,375.38 -	1,375.38	504.36	03/2021 -	03/2024	36(O) -	8/10
97	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]MCL,ODISHA ,	05/2018	2,434.75 -	2,434.75	181.04	03/2027 -	03/2027	0(O) -	3/12
98	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]MCL,ODISHA ,	11/2018	2,838.87 -	2,838.87	1,236.90	03/2029 -	03/2029	0(O) -	0/9
99	TALABIRA II AND III OCP - [N06000189]NLC,ODISHA , Central Sector Projects	07/2017	2,401.07 -	2,401.07	861.37	07/2020 -	04/2020	-	18/22
100	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN , Central Sector Projects	03/2015	522.45 -	522.45	9.88	09/2019 -	-	-	0/0
101	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN , Central Sector Projects	03/2015	513.63 -	513.63	175.30	12/2019 -	-	-	0/0
102	BARSINGSAR THERMAL POWER STATION EXTENSION - [N06000187]NLC,RAJASTHAN , Central Sector Projects	03/2015	2,112.60 -	2,112.60	140.80	09/2020 -	-	-	0/0
103	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188]NLC,RAJASTHAN , Central Sector Projects	03/2015	2,196.30 -	2,196.30	140.80	09/2020 -	-	-	0/0
104	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU ,	06/2011	5,907.11 7,980.79	7,980.79	7,405.84	12/2015 -	02/2021	-	35/35
105	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU ,	04/2013	1,458.17 709.06	709.06	484.81	06/2015 03/2025	03/2025	117(O) 0	5/7
106	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA ,	12/2009	418.97 -	489.62	416.07	03/2012 -	03/2023	132(O) -	1/2
107	KISTARAM OCP - [N06000089]SCCL,TELANGANA ,	11/2010	242.29 -	164.04	129.58	03/2015 -	03/2022	84(O) -	4/5
108	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA ,	07/2011	162.76 -	349.28	251.14	03/2015 -	03/2022	84(O) -	12/29
109	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA ,	07/2011	447.06 -	473.22	79.04	03/2015 -	03/2023	96(O) -	10/13
110	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA ,	07/2012	417.33 -	384.32	131.62	07/2016 -	03/2022	68(O) -	26/28
111	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA ,	11/2012	430.45 -	415.37	193.76	03/2016 -	03/2021	-	38/39

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
112	KAKATIYAKHANI OPENCASE-2 PROJECT - [N06000129]SCCL,TELANGANA ,	05/2015	397.09 -	442.42	109.25	03/2019 -	03/2022	36(O) -	17/18
113	KAKATIYAKHANI OPENCASE III PROJECT PHASE-1 - [N06000161]SCCL,TELANGANA ,	03/2017	413.84 -	413.84	230.95	03/2019 -	03/2022	36(O) -	6/11
114	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL,TELANGANA ,	11/2016	272.73 -	272.73	153.75	-	03/2022	-	2/6
115	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH ,	07/2016	17,237.00 -	17,237.80	11,574.21	11/2021 07/2022	07/2022	8(O) 0	11/48
116	EXPANSION PR OF JHANJRA UG(5.00 MTY) - [N06000020]ECL,WEST BENGAL ,	11/2015	1,210.12 -	1,210.12	26.05	03/2022 03/2029	03/2029	84(O) 0	9/13
117	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL ,	08/2012	1,055.05 -	1,055.05	669.82	03/2018 -	10/2021	43(O) -	12/16
118	RANIGANJ MASTER PLAN - [N06000163]ECL,WEST BENGAL ,	08/2009	2,661.73 -	5,146.48	621.70	08/2019 -	-	-	1/19
119	SIDULI MINE (OC AND UG) - [N06000165]ECL,WEST BENGAL ,	05/2018	535.18 -	535.18	1.39	03/2026 -	03/2026	0(O) -	4/22
120	NAKRAKONDA KUMARDIH B OCP - [N06000170]ECL,WEST BENGAL ,	08/2018	502.68 -	502.68	12.62	03/2029 -	03/2029	0(O) -	1/22
121	TILABONI UG MINE - [N06000172]ECL,WEST BENGAL ,	02/2019	916.62 -	916.62	.61	03/2027 -	03/2027	0(O) -	1/27
122	PARASEA- BELBAID REORGANISATION UG MINE - [N06000185]ECL,WEST BENGAL ,	07/2019	826.42 -	826.42	.03	03/2027 -	03/2027	0(O) -	0/22
123	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT - [N06000191]ECL,WEST BENGAL ,	04/2020	483.65 -	483.65	1.82	03/2025 -	03/2025	0(O) -	0/0
124	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]BCCL,WEST BENGAL ,	12/2015	304.13 341.22	341.22	40.84	03/2017 -	03/2022	60(O) -	0/0
	Total		1,45,653.01 -	1,44,995.00	49,331.74				474/989
	<u>FINANCE</u>								
125	C/O OF 152 NOS TYPE-II 304 NOS TYPE-III 76 NOS TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD,TAMIL NADU ,	12/2015	209.00 -	208.96	205.72	10/2019 -	07/2021	21(O) -	1/6
126	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU ,	11/2017	348.77 -	348.77	123.99	11/2021 -	11/2021	0(O) -	2/8
	Total		557.77 -	557.73	329.71				3/14
	<u>FERTILISERS</u>								
127	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]NFL,HARYANA ,	01/2018	215.92 -	215.92	168.30	11/2019 06/2021	05/2021	18(O) 1	0/2
128	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]RCF,MAHARASHTRA ,	04/2018	426.72 -	426.72	288.80	04/2020 03/2021	07/2021	15(O) 2	12/14
129	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]NFL,PUNJAB ,	01/2018	218.83 -	218.83	191.30	11/2019 05/2021	04/2021	17(O) 0	1/2

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
130	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]NFL,PUNJAB ,	01/2018	239.81 -	239.81	199.11	11/2019 05/2021	04/2021	17(O) 0	1/2
	Total		1,101.28 -	1,101.28	847.51				14/20
	<u>MINES</u>								
131	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]NALCO,ODISHA ,	12/2014	5,540.00 6,435.90	5,540.00	731.55	04/2021 12/2022	12/2022	20(O) 0	4/4
132	UTKAL D AND E COAL BLOCK - [N10000011]NALCO,ODISHA ,	05/2016	534.00 -	534.00	338.79	01/2020 -	-	-	2/3
133	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]NALCO,ODISHA , Central Sector Projects	12/2015	355.00 -	355.00	94.80	11/2020 -	02/2021	-	3/3
134	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]NALCO,ODISHA , Central Sector Projects	11/2017	483.00 483.00	483.00	.92	04/2021 03/2023	03/2023	23(O) 0	2/2
135	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]NALCO,TAMIL NADU ,	09/2017	166.62 163.17	163.17	135.00	06/2019 06/2021	12/2020	-	1/1
	Total		7,078.62 -	7,075.17	1,301.06				12/13
	<u>STEEL</u>								
136	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH ,	12/2011	2,858.00 -	2,558.00	1,838.96	12/2017 12/2021	12/2021	48(O) 12	5/6
137	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH ,	01/2010	15,525.00 21,940.00	21,940.00	18,516.49	05/2015 07/2021	07/2021	74(O) 0	70/86
138	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP - [N12000123]SAIL,CHHATISGARH ,	11/2020	542.24 -	542.24	31.68	12/2023 -	12/2023	0(O) -	0/0
139	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 - [N12000124]NMDC,CHHATISGARH , Central Sector Projects	11/2015	2,907.00 -	2,907.00	256.24	06/2023 -	06/2023	0(O) -	0/8
140	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND ,	03/2015	1,034.01 -	1,034.01	537.82	10/2017 12/2021	12/2021	50(O) 0	0/2
141	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND ,	11/2016	262.87 -	262.87	185.85	06/2019 05/2021	08/2021	26(O) 3	1/1
142	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY - [N12000122]SAIL,ODISHA ,	11/2020	377.18 -	377.18	32.76	05/2023 -	05/2023	0(O) -	0/1
143	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH ,	04/2014	1,682.85 -	1,682.85	1,564.62	09/2018 06/2021	06/2021	33(O) 2	5/5
144	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E - [N12000121]SAIL,WEST BENGAL ,	12/2018	263.36 -	263.36	215.38	09/2020 03/2021	09/2021	12(O) 4	1/4
	Total		25,452.51 -	31,567.51	23,179.80				82/113
	<u>PETROLEUM</u>								

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
145	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH ,	07/2016	20,928.00 26,264.00	26,264.00	14,820.38	07/2020 07/2022	07/2022	24(O) 0	93/111
146	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH ,	03/2016	34,012.00 -	25,090.00	11,254.33	06/2020 06/2022	06/2022	24(O) 0	15/20
147	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL AP - [N16000302]IOCL,ANDHRA PRADESH ,	08/2017	384.58 -	384.58	248.75	04/2021 03/2021	03/2021	-	0/0
148	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH ,	08/2018	466.00 -	466.00	256.49	04/2021 12/2021	12/2021	8(O) 5	0/0
149	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH ,	04/2018	355.00 -	355.00	106.53	04/2022 -	02/2023	10(O) -	0/0
150	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]IOCL,ANDHRA PRADESH ,	10/2018	316.20 -	316.20	98.14	10/2021 03/2022	03/2022	5(O) 5	0/0
151	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364]BPCL,ANDHRA PRADESH ,	07/2017	580.20 -	580.20	155.84	02/2021 -	03/2023	25(O) -	0/16
152	SWRO II WITH LLPH FACILITIES - [N16000378]HPCL,ANDHRA PRADESH ,	09/2019	196.26 -	196.26	92.38	07/2020 -	07/2021	12(O) -	1/5
153	LPG BP PROJECT CHITTOOR - [N16000381]IOCL,ANDHRA PRADESH ,	07/2019	167.00 -	167.00	8.89	07/2022 -	07/2022	0(O) -	0/0
154	RUF PITCH LOADING GANTRY - [N16000406]HPCL,ANDHRA PRADESH , EPC	10/2020	332.61 -	332.61	.01	11/2022 -	11/2022	0(O) -	0/0
155	220 KV GRID SUPPLY - [N16000407]HPCL,ANDHRA PRADESH , EPC	10/2020	303.40 -	303.40	199.17	03/2021 -	-	-	0/0
156	SULPHUR FORMING UNIT IN SRU - [N16000408]HPCL,ANDHRA PRADESH , EPC	10/2020	210.94 -	210.94	117.03	08/2021 -	08/2021	0(O) -	0/0
157	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) CACHAR ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM ,	06/2016	423.00 -	502.00	422.12	08/2019 06/2021	06/2021	22(O) 0	8/13
158	PIPELINE NETWORK PROJECT GELEKI ASSAM - [N16000278]ONGC,ASSAM ,	07/2016	249.85 303.75	303.75	199.31	05/2020 05/2021	05/2021	12(O) 0	4/5
159	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM ,	01/2018	543.91 -	652.10	320.30	02/2020 -	06/2021	16(O) -	1/14
160	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]IOCL,ASSAM ,	08/2018	557.00 -	557.00	496.45	02/2020 06/2021	06/2021	16(O) 0	5/5
161	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS MADHUBAN - [N16000356]OIL,ASSAM ,	06/2016	224.75 -	222.21	166.48	08/2020 -	06/2021	10(O) -	0/0
162	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTA REFINARY - [N16000379]NRL,ASSAM ,	01/2019	12,366.00 -	12,366.00	168.82	10/2024 -	10/2024	0(O) -	0/0
163	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES - [N16000394]NRL,ASSAM ,	01/2019	10,228.00 -	10,228.00	117.34	10/2024 -	10/2024	0(O) -	0/0
164	LPG BP PROJECT MOTIHARI - [N16000317]IOCL,BIHAR ,	05/2018	206.50 -	206.50	134.97	03/2021 09/2021	09/2021	6(O) 0	18/26
165	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]IOCL,BIHAR ,	12/2017	199.36 -	199.36	34.40	10/2020 08/2022	08/2022	22(O) 0	2/2
166	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]GAIL,BIHAR ,	10/2017	359.25 -	359.25	143.73	10/2022 -	10/2022	0(O) -	10/10

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
167	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]OCL,BIHAR ,	07/2018	189.00 -	189.00	149.34	01/2021 06/2021	06/2021	5(O) 0	6/8
168	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI BIHAR - [N16000344]OCL,BIHAR ,	04/2018	522.00 -	522.00	323.87	03/2021 12/2021	12/2021	9(O) 0	0/0
169	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA - [N16000386]OCL,BIHAR ,	01/2020	14,810.00 -	14,810.00	934.70	04/2023 -	04/2023	0(O) -	2/2
170	MUZAFFARPUR-MOTIHARI LPG PIPELINE - [N16000399]OCL,BIHAR ,	06/2020	403.00 -	403.00	1.77	08/2022 -	08/2022	0(O) -	0/0
171	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT ,	04/2016	327.78 -	200.00	196.50	04/2018 -	06/2021	38(O) -	19/20
172	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]ONGC,GUJARAT ,	02/2017	1,162.56 -	970.30	832.63	03/2026 -	03/2026	0(O) -	7/10
173	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]OCL,GUJARAT ,	10/2017	906.00 -	906.00	279.82	02/2020 10/2021	10/2021	20(O) 0	7/8
174	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA GUJARAT - [N16000336]OCL,GUJARAT ,	03/2018	588.20 730.20	730.20	77.30	- 05/2023	05/2023	- 0	11/17
175	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]GAIL,GUJARAT ,	09/2018	225.54 247.90	247.90	40.10	02/2021 -	12/2021	10(O) -	5/8
176	LAB REVAMP AT GUJARAT REFINERY - [N16000377]OCL,GUJARAT , Central Sector Projects	10/2019	403.00 -	403.00	103.74	12/2021 -	12/2021	0(O) -	8/11
177	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY - [N16000382]OCL,GUJARAT ,	11/2019	5,251.00 -	5,251.00	192.50	05/2023 -	05/2023	0(O) -	3/11
178	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400]OCL,GUJARAT ,	06/2020	1,378.00 -	1,378.00	24.39	12/2022 -	12/2022	0(O) -	0/0
179	REDEVELOPMENT OF NANDASAN FIELD - [N16000404]ONGC,GUJARAT ,	02/2020	444.87 -	444.87	87.40	08/2022 -	08/2022	0(O) -	0/0
180	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY - [N16000409]OCL,GUJARAT , Central Sector Projects	09/2020	18,936.00 -	18,936.00	715.09	09/2024 -	09/2024	0(O) -	0/0
181	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM - [N16000411]OCL,GUJARAT ,	10/2020	1,614.00 -	1,614.00	.00	08/2023 -	08/2023	0(O) -	0/0
182	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]HPCL,HARYANA ,	11/2017	255.00 300.00	300.00	271.70	11/2020 06/2021	06/2021	7(O) 0	45/46
183	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]OCL,HARYANA ,	04/2018	206.63 -	206.63	93.11	02/2020 08/2021	08/2021	18(O) 0	5/7
184	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]OCL,HARYANA ,	08/2018	1,636.00 -	1,636.00	723.59	08/2020 04/2022	04/2022	20(O) 0	6/7
185	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]OCL,HARYANA ,	01/2019	909.00 -	909.00	309.94	01/2021 03/2022	03/2022	14(O) 0	2/6
186	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]OCL,HARYANA ,	10/2018	598.00 -	598.00	293.80	02/2020 02/2022	02/2022	24(O) 0	4/5
187	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]GAIL,HARYANA ,	08/2018	286.42 327.01	327.01	186.00	08/2020 05/2021	06/2021	10(O) 0	13/16
188	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV PANIPAT - [N16000363]OCL,HARYANA ,	12/2018	278.60 -	278.60	44.73	06/2021 07/2022	07/2022	13(O) 0	1/3

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
189	R and D CAMPUS II AT FARIDABAD - [N16000375]IOCL,HARYANA ,	06/2019	2,281.94 -	2,281.94	431.31	12/2022 07/2023	07/2023	7(O) 0	0/0
190	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]IOCL,HARYANA ,	08/2019	1,255.00 -	1,255.00	185.11	10/2021 -	10/2021	0(O) -	0/0
191	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383]IOCL,HARYANA ,	09/2019	164.69 -	164.69	13.16	07/2021 03/2022	03/2022	8(O) 0	0/0
192	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS - [N16000385]HPCL,HARYANA , EPC	09/2018	520.00 -	520.00	126.72	09/2026 02/2027	02/2027	5(O) 0	0/0
193	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]ONGC,JHARKHAND ,	12/2015	823.27 1,137.79	1,137.79	669.73	03/2023 03/2022	03/2022	-12(O) 0	6/10
194	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]HPCL,JHARKHAND ,	06/2017	161.50 -	161.50	78.18	06/2020 09/2021	09/2021	15(O) 0	4/12
195	CITY GAS DISTRIBUTION (CGD) NETWORK RANCHI - [N16000329]GAIL,JHARKHAND ,	10/2017	226.45 -	226.45	110.99	10/2022 -	10/2022	0(O) -	19/19
196	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]BPCL,JHARKHAND ,	11/2018	248.55 -	248.55	109.38	06/2022 -	06/2022	0(O) -	0/0
197	CITY GAS DISTRIBUTION JAMSHEDPUR - [N16000389]GAIL,JHARKHAND ,	10/2017	221.45 -	221.45	92.99	10/2022 -	10/2022	0(O) -	9/9
198	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA ,	09/2016	1,810.00 1,810.00	1,810.00	1,658.31	12/2019 04/2021	02/2022	26(O) 4	9/10
199	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA , Central Sector Projects	11/2017	581.00 637.00	637.00	489.10	03/2020 11/2020	07/2021	16(O) 1	2/3
200	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]BPCL,KARNATAKA ,	10/2018	206.26 -	206.26	132.84	03/2021 -	05/2021	2(O) -	0/15
201	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367]HPCL,KARNATAKA ,	06/2019	2,166.38 -	2,166.38	922.06	06/2022 -	06/2022	0(O) -	12/18
202	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369]HPCL,KARNATAKA ,	12/2018	854.00 -	854.00	150.14	12/2022 -	12/2022	0(O) -	13/19
203	SETTING UP OF PHASE LL FACILITIES FOR HPCL GREEN R AND D CENTRE AT BENGALURU - [N16000380]HPCL,KARNATAKA ,	06/2018	380.00 -	380.00	222.20	11/2021 -	11/2021	0(O) -	11/19
204	DEVANGONTHI MARKETING TERMINAL - [N16000401]MANGALORE REFIN,KARNATAKA ,	06/2020	200.00 -	200.00	2.26	06/2023 -	06/2023	0(O) -	1/6
205	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA ,	10/2015	607.06 1,236.00	1,236.00	394.74	10/2017 03/2022	03/2022	53(O) 0	44/52
206	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA ,	11/2014	4,588.29 5,245.96	5,245.96	5,076.00	08/2018 11/2019	05/2021	33(O) 0	0/20
207	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA ,	02/2016	3,313.00 -	3,288.96	2,967.01	02/2020 03/2021	05/2021	15(O) 0	0/20
208	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA ,	12/2015	1,112.00 1,507.24	1,507.24	730.00	06/2019 -	02/2022	32(O) -	0/0
209	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]BPCL,KERALA ,	09/2018	11,130.00 -	11,130.00	379.09	03/2023 -	03/2023	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
210	PROVISION OF 2ND SPUR FOR TWL GANTRY TWD FACILITY FOR MS AND HSD ADDITIONAL TANKS FOR MS HSD AND - [N16000304]IOCL, MADHYA PRADESH ,	08/2017	236.00 293.00	293.00	161.05	06/2020 09/2021	09/2021	15(O) 0	0/0
211	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC, MAHARASHTRA ,	03/2011	861.79 1,846.46	2,001.00	1,551.48	05/2013 02/2022	02/2022	105(O) 11	5/8
212	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC, MAHARASHTRA , Central Sector Projects	12/2015	3,190.69 3,375.90	3,375.90	2,786.78	04/2018 05/2022	05/2022	49(O) 12	13/15
213	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL, MAHARASHTRA ,	05/2016	1,945.00 -	1,945.00	1,536.61	02/2022 -	02/2022	0(O) -	5/5
214	MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL, MAHARASHTRA ,	04/2013	449.58 -	449.58	396.13	12/2019 04/2021	04/2021	16(O) 0	0/17
215	ADDITIONAL FACILITIES AT MANMAD FOR COVERION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL, MAHARASHTRA ,	05/2016	212.00 -	212.00	148.29	01/2021 -	09/2021	8(O) -	0/0
216	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL, MAHARASHTRA ,	05/2016	348.00 -	348.00	217.55	01/2021 -	10/2021	9(O) -	0/0
217	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELI - [N16000276]IOCL, MAHARASHTRA ,	05/2016	261.00 -	261.00	158.24	01/2021 -	09/2021	8(O) -	0/0
218	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL, MAHARASHTRA ,	09/2015	4,199.00 5,060.00	5,060.00	4,528.82	03/2020 -	-	-	122/135
219	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]ONGC, MAHARASHTRA ,	02/2017	4,006.83 4,475.92	3,596.00	3,514.02	05/2021 05/2021	05/2021	0(O) 0	14/15
220	PUNE POL STORAGE DEPOT - [N16000313]BPCL, MAHARASHTRA ,	08/2016	282.64 -	282.64	246.11	08/2020 -	03/2021	-	0/15
221	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD) MAHARASHTRA - [N16000315]HPCL, MAHARASHTRA ,	06/2017	249.26 -	249.26	134.44	06/2020 12/2021	09/2021	15(O) 0	3/12
222	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3 D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]ONGC, MAHARASHTRA ,	02/2019	2,292.46 -	2,203.71	1,757.87	05/2021 12/2021	12/2021	7(O) 7	4/6
223	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]ONGC, MAHARASHTRA ,	04/2019	3,228.80 3,976.67	3,976.67	1,188.33	03/2022 05/2023	05/2023	14(O) 0	4/6
224	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]ONGC, MAHARASHTRA ,	05/2019	3,660.71 3,740.05	3,740.05	2,808.52	05/2021 01/2022	01/2022	8(O) 8	4/6
225	HEERA REDEVELOPMENT - PHASE III - [N16000360]ONGC, MAHARASHTRA ,	06/2019	2,494.68 -	2,354.72	1,421.11	03/2022 -	03/2022	0(O) -	4/6
226	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]ONGC, MAHARASHTRA ,	05/2019	763.92 -	733.86	757.62	12/2020 05/2021	05/2021	5(O) 0	4/5
227	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY - [N16000397]BPCL, MAHARASHTRA ,	07/2020	640.00 -	640.00	326.57	12/2021 -	12/2021	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
228	KEROSENE HYDROTREATER (KHT) UNIT INTEGRATED WITH EXISTING DIESEL HYDROTREATER (DHT) UNIT AT MUMBAI R - [N16000410]BPCL,MAHARASHTRA ,	08/2020	697.00 -	697.00	155.18	03/2023 -	03/2023	0(O) -	0/0
229	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE ,	07/2011	352.56 -	490.24	455.00	03/2017 -	03/2021	-	2/15
230	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE ,	01/2015	1,823.00 3,027.90	3,027.90	1,957.55	03/2021 12/2021	12/2021	9(O) 4	5/5
231	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE ,	01/2015	2,321.00 3,338.00	3,338.00	2,923.70	12/2020 03/2022	03/2022	15(O) 0	5/5
232	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE ,	01/2015	690.00 -	690.00	545.44	07/2018 05/2021	05/2021	34(O) 0	27/36
233	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE ,	05/2016	406.00 -	406.00	225.67	10/2020 -	03/2022	17(O) -	6/12
234	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE ,	09/2016	571.66 -	571.66	471.81	12/2019 -	08/2021	20(O) -	6/22
235	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE ,	07/2015	2,881.40 -	2,000.00	1,607.70	12/2020 -	09/2021	9(O) -	21/24
236	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]GAIL,MULTI STATE ,	03/2017	2,433.00 -	2,433.00	2,110.70	12/2020 12/2021	06/2021	6(O) 0	20/24
237	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]GAIL,MULTI STATE ,	03/2017	3,437.00 3,048.00	3,048.00	1,852.90	12/2020 12/2021	12/2021	12(O) 0	19/24
238	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE , Central Sector Projects	06/2009	2,915.00 5,909.00	5,909.00	3,607.20	12/2012 02/2022	02/2022	110(O) 0	26/42
239	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]HPCL,MULTI STATE ,	09/2017	2,677.00 -	3,072.00	2,239.96	06/2021 08/2022	08/2022	14(O) 0	18/26
240	BARAUNI-GUWAHATI PIPELINE - [N16000334]GAIL,MULTI STATE ,	06/2018	3,308.00 3,060.00	3,060.00	2,272.30	12/2021 -	12/2021	0(O) -	16/20
241	BARMER PALANPUR PIPELINE - [N16000384]HPCL,MULTI STATE , Central Sector Projects	11/2019	776.00 -	776.00	215.96	11/2022 -	11/2022	0(O) -	11/20
242	SRIKAKULAM ANGUL PIPELINE PROJECT - [N16000388]GAIL,MULTI STATE ,	09/2019	2,658.34 -	2,658.34	245.50	07/2022 -	07/2022	0(O) -	8/14
243	DHAMRA HALDIA PIPELINE PROJECT - [N16000391]GAIL,MULTI STATE ,	03/2020	1,030.65 -	1,030.65	53.10	11/2022 -	11/2022	0(O) -	7/12
244	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT - [N16000398]GAIL,MULTI STATE ,	06/2020	7,844.25 -	7,844.25	1,079.10	05/2023 -	05/2023	0(O) -	8/29
245	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]GAIL,ODISHA ,	03/2017	1,933.00 -	1,933.00	1,268.75	12/2020 12/2021	12/2021	12(O) 0	19/24
246	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA , Central Sector Projects	12/2016	161.59 -	161.59	49.59	12/2019 03/2022	03/2022	27(O) 0	18/26
247	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL,ODISHA , Central Sector Projects	07/2017	243.53 -	243.53	115.28	07/2022 -	07/2022	0(O) -	10/10

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
248	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]IOCL,ODISHA ,	08/2017	315.00 -	315.00	208.09	12/2021 -	08/2021	-4(O) -	3/3
249	CITY GAS DISTRIBUTION (CGD) NETWORK CUTTACK - [N16000328]GAIL,ODISHA ,	07/2017	182.20 -	182.20	78.03	07/2022 -	07/2022	0(O) -	9/9
250	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]IOCL,ODISHA ,	04/2018	5,654.00 -	5,654.00	2,826.29	10/2021 -	10/2021	0(O) -	7/10
251	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]IOCL,ODISHA ,	10/2018	1,297.50 -	1,297.50	722.93	10/2021 -	03/2022	5(O) -	1/1
252	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]IOCL,ODISHA ,	11/2018	462.30 -	462.30	23.19	09/2021 06/2022	06/2022	9(O) 0	1/5
253	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]IOCL,ODISHA ,	05/2019	3,361.00 -	3,361.00	1,665.03	08/2021 09/2022	09/2022	13(O) 13	7/11
254	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]IOCL,ODISHA ,	06/2019	371.00 -	371.00	4.44	09/2022 03/2023	03/2023	6(O) 0	1/8
255	2ND GENERATION LIGNOCELLUOSIC BIOMASS ETHANOL BIOFUEL REFINERY AT BARGARH (ODISHA) - [N16000374]BPCL,ODISHA ,	08/2019	1,607.00 -	1,607.00	255.22	08/2022 -	08/2022	0(O) -	0/21
256	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY - [N16000395]IOCL,ODISHA , Central Sector Projects	01/2020	202.16 -	202.16	18.34	07/2022 -	07/2022	0(O) -	0/0
257	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY - [N16000396]IOCL,ODISHA , Central Sector Projects	07/2020	13,805.00 -	13,805.00	92.75	01/2024 -	01/2024	0(O) -	0/0
258	SECOND GENERATION ETHANOL BIOREFINERY PROJECT BATHINDA PUNJAB - [N16000402]HPCL,PUNJAB ,	05/2020	1,421.46 -	1,244.50	76.19	02/2023 -	02/2023	0(O) -	7/22
259	LPG BP PROJECT JODHPUR - [N16000318]IOCL,RAJASTHAN ,	03/2018	229.80 -	229.80	81.48	- 05/2022	05/2022	- 0	17/26
260	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU ,	05/2013	711.00 -	711.00	11.12	06/2020 -	-	-	0/0
261	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU ,	11/2012	678.00 1,472.00	1,472.00	19.44	02/2017 08/2022	08/2022	66(O) 0	0/0
262	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU ,	11/2015	650.82 -	624.35	447.05	03/2019 09/2021	09/2021	30(O) 4	4/5
263	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU ,	05/2016	4,497.00 6,025.00	6,025.00	3,681.97	12/2018 02/2022	02/2022	38(O) 0	5/5
264	AUGMENTATION OF CTMPL - [N16000286]IOCL,TAMIL NADU , Central Sector Projects	12/2016	228.00 -	228.00	140.61	11/2021 -	11/2021	0(O) -	5/5
265	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU ,	09/2017	1,858.00 -	1,858.00	1,528.75	12/2019 -	-	-	0/0
266	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU ,	08/2017	421.00 -	300.00	241.01	08/2020 -	09/2021	13(O) -	0/0
267	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR TAMIL NADU - [N16000305]IOCL,TAMIL NADU ,	12/2017	466.43 -	466.43	207.05	10/2020 01/2022	01/2022	15(O) 5	0/0
268	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT CHENNAI - [N16000403]IOCL,TAMIL NADU ,	10/2020	921.00 -	921.00	19.14	09/2023 -	09/2023	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
269	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU CHENNAI AS RESITEMENT OF EXISTING FACI - [N16000405]IOCL,TAMIL NADU , EPC	10/2020	1,398.00 -	1,398.00	80.68	12/2023 -	05/2023	-7(O) -	0/0
270	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA ,	12/2018	611.00 -	611.00	76.47	04/2022 -	08/2023	16(O) -	0/0
271	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]GAIL,UTTAR PRADESH , Central Sector Projects	04/2017	287.49 345.15	345.15	200.77	04/2022 -	04/2022	0(O) -	43/43
272	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH ,	08/2017	318.80 -	318.80	147.52	08/2021 -	11/2021	3(O) -	0/0
273	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]IOCL,UTTAR PRADESH ,	08/2017	255.40 -	255.40	64.34	08/2020 11/2021	11/2021	15(O) 0	1/1
274	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]IOCL,UTTAR PRADESH ,	03/2018	676.00 -	676.00	433.41	08/2022 -	08/2022	0(O) -	3/3
275	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL - [N16000365]BPCL,UTTAR PRADESH ,	12/2017	1,524.06 -	1,524.06	785.64	12/2021 -	12/2021	0(O) -	0/21
276	CITY GAS DISTRIBUTION IN UP AND UK - [N16000387]HPCL,UTTAR PRADESH ,	03/2019	3,450.20 -	3,450.20	235.43	03/2029 08/2029	08/2029	5(O) 0	0/0
277	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT - [N16000390]GAIL,UTTAR PRADESH ,	08/2018	217.92 217.92	217.92	89.80	04/2021 -	10/2021	6(O) -	12/14
278	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND , Central Sector Projects	02/2017	160.10 -	160.10	93.54	02/2020 06/2021	06/2021	16(O) 0	19/26
279	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]GAIL,WEST BENGAL ,	03/2017	1,740.00 -	1,740.00	764.50	12/2020 12/2021	12/2021	12(O) 0	13/24
280	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL,WEST BENGAL ,	04/2017	163.02 -	163.02	101.52	04/2020 10/2021	10/2021	18(O) 0	18/26
281	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]IOCL,WEST BENGAL ,	03/2018	3,712.00 -	3,696.00	1,995.95	09/2022 -	03/2022	-6(O) -	3/3
282	CITY GAS DISTRIBUTION IN WEST BENGAL - [N16000392]HPCL,WEST BENGAL , EPC	03/2019	5,830.20 -	5,830.20	93.97	03/2031 08/2029	08/2029	-19(O) 0	0/0
283	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY - [N16000393]IOCL,WEST BENGAL ,	06/2020	1,019.00 -	1,019.00	58.94	01/2023 -	01/2023	0(O) -	0/0
	Total		2,96,976.45 -	3,04,256.68	1,15,047.73				1044/1577
	POWER								
284	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH ,	09/2003	6,285.33 19,992.43	19,992.43	13,732.39	09/2010 08/2023	08/2023	155(O) 0	0/0
285	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH ,	12/2004	2,496.90 7,927.34	7,927.34	8,225.88	12/2009 02/2021	-	-	30/30
286	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR ,	02/2005	8,692.97 21,312.11	21,312.11	18,595.56	10/2011 07/2023	07/2023	141(O) 0	33/48

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
287	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR ,	01/2007	5,353.00 10,566.00	10,566.00	8,847.06	07/2012 06/2020	07/2021	108(O) 1	14/25
288	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR , Joint Venture	01/2013	12,964.60 17,304.00	17,304.00	15,787.92	05/2018 -	12/2021	43(O) -	43/45
289	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]SJVN,BIHAR ,	03/2019	10,439.09 10,439.09	10,439.09	2,035.50	01/2024 -	01/2024	0(O) -	16/27
290	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH ,	12/2012	11,846.00 -	12,739.82	13,766.78	10/2017 -	-	-	41/41
291	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH ,	09/2015	3,004.00 -	3,004.00	2,464.37	11/2019 -	-	-	0/0
292	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI ,	03/2015	1,394.52 -	1,394.52	534.89	05/2017 09/2021	09/2021	52(O) 3	4/9
293	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI ,	10/2017	271.90 -	271.90	240.96	11/2019 -	06/2021	19(O) -	0/0
294	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT , Central Sector Projects	05/2017	175.64 -	175.64	122.47	09/2018 11/2020	09/2020	-	0/0
295	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPPT AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT ,	12/2017	193.14 -	193.14	123.36	06/2019 11/2020	09/2020	-	0/0
296	KAWAS SOLAR 56 MW - [N18000283]NTPC,GUJARAT , EPC	08/2020	261.80 -	261.80	.00	10/2021 -	10/2021	0(O) -	0/0
297	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH ,	09/2002	3,919.59 9,897.59	9,897.59	8,945.10	09/2009 07/2022	07/2022	154(O) 0	5/5
298	LUHRI HYDROELECTRIC PROJECT (STAGE1) - [N18000279]SJVN,HIMACHAL PRADESH ,	11/2020	1,810.56 -	1,810.56	422.46	01/2026 -	01/2026	0(O) -	0/0
299	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR ,	10/2014	8,112.12 -	8,112.12	1,766.91	04/2020 -	07/2025	63(O) -	0/0
300	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND ,	02/2014	14,366.58 -	15,389.42	11,722.10	06/2019 10/2022	10/2022	40(O) 0	29/30
301	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND ,	10/2004	4,237.96 4,238.00	4,552.00	3,601.54	10/2017 -	-	-	0/0
302	PATRATU STPP-I (3X800MW) - [N18000275]NTPC,JHARKHAND ,	11/2017	18,668.00 -	17,112.00	4,351.86	03/2023 -	09/2024	18(O) -	3/7
303	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA , Central Sector Projects	05/2017	445.89 675.73	675.73	463.08	02/2019 02/2021	02/2021	-	0/0
304	KAYAMKULAM SOLAR 70 MW - [N18000288]NTPC,KERALA , EPC	09/2019	403.62 -	403.62	53.13	06/2021 10/2021	10/2021	4(O) 0	0/0
305	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH ,	03/2013	11,638.55 -	15,105.22	13,657.43	01/2018 -	02/2021	-	43/43
306	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC,MADHYA PRADESH ,	03/2015	9,870.51 -	11,148.86	10,019.31	01/2020 -	-	-	41/41
307	AMELIA COAL MINE - [N18000252]THDCIL,MADHYA PRADESH , Central Sector Projects	01/2017	2,104.21 -	1,587.16	495.58	09/2020 08/2022	08/2022	23(O) 0	10/16
308	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA ,	03/2012	7,921.47 -	7,921.47	5,302.00	09/2016 -	-	-	41/41
309	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR ,	12/1999	578.62 -	578.62	.00	06/2006 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
310	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE ,	10/2008	4,824.12 5,071.94	5,071.94	4,634.56	10/2012 11/2020	03/2021	-	8/11
311	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE ,	02/2009	11,130.19 14,719.10	14,719.10	12,894.95	08/2013 08/2022	08/2022	108(O) 0	23/26
312	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE ,	10/2011	487.49 -	639.46	590.30	06/2014 -	-	-	10/12
313	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE ,	10/2013	1,364.52 1,891.41	1,891.41	1,326.81	04/2016 09/2020	07/2020	-	12/12
314	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE ,	01/2014	374.63 -	374.63	246.80	04/2016 12/2017	06/2021	62(O) 0	0/0
315	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE ,	05/2014	522.29 546.36	546.36	478.29	11/2016 09/2021	06/2021	55(O) 1	10/12
316	TRANSMISSION SYSTEM STRENGTHENING IN WR- NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE ,	06/2014	5,151.37 -	5,151.37	3,269.93	03/2018 -	-	-	9/12
317	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE ,	01/2015	871.62 902.49	902.49	648.77	10/2017 05/2021	01/2021	-	5/5
318	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE ,	01/2015	203.28 -	260.03	200.16	07/2017 -	-	-	3/5
319	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE ,	03/2015	197.40 -	197.40	90.05	03/2018 -	06/2021	39(O) -	0/0
320	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE ,	03/2016	808.63 -	808.63	662.19	01/2018 04/2021	05/2021	40(O) 1	0/0
321	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE ,	05/2016	3,519.59 -	3,519.59	2,562.41	05/2019 -	-	-	0/0
322	HVDC BIPOLE LINK BETWEEN WR (RAIGARH CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE ,	05/2016	14,733.37 -	14,733.37	11,552.37	11/2019 04/2021	06/2021	19(O) 2	0/0
323	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE ,	03/2017	283.72 -	283.72	196.10	11/2019 -	-	-	0/0
324	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE ,	10/2016	408.46 516.12	516.12	417.12	01/2019 09/2020	04/2020	-	0/0
325	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE ,	10/2016	608.24 -	608.24	425.04	04/2019 -	-	-	0/0
326	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE ,	02/2017	322.30 -	322.30	201.55	02/2019 06/2021	09/2021	31(O) 3	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
327	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE ,	02/2017	235.53 -	235.53	151.12	06/2019 08/2021	06/2021	24(O) 1	0/0
328	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE ,	03/2017	379.95 -	379.95	232.02	12/2019 06/2021	09/2021	21(O) 3	0/0
329	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH CHATTISGARH) AND SOUTHERN REGION (PUGALAR TM) NOR - [N18000247]PGCIL,MULTI STATE ,	02/2017	5,070.13 -	5,070.13	4,101.57	04/2020 06/2021	06/2021	14(O) 0	0/0
330	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE ,	12/2014	4,754.42 9,129.32	9,129.32	2,163.30	12/2018 -	03/2024	63(O) -	0/0
331	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE ,	12/2014	5,111.33 6,700.00	6,700.00	2,767.14	12/2018 -	12/2021	36(O) -	0/0
332	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE , Central Sector Projects	12/2015	3,654.00 -	3,654.00	3,508.04	04/2019 -	-	-	0/0
333	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE , Central Sector Projects	03/2017	3,500.00 3,500.00	3,994.00	2,917.31	07/2020 12/2020	06/2021	11(O) 1	0/0
334	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE , Central Sector Projects	08/2017	1,931.39 -	1,931.39	1,709.25	02/2020 06/2021	06/2021	16(O) 0	0/0
335	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE ,	09/2017	198.49 -	198.49	140.97	09/2019 09/2020	05/2020	-	0/0
336	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE ,	11/2017	358.83 -	358.83	253.49	05/2020 05/2021	05/2021	12(O) 1	0/0
337	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA ,	02/2014	12,532.44 13,140.91	13,140.91	11,730.23	12/2018 05/2021	05/2021	29(O) 0	40/42
338	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC,ODISHA ,	05/2016	1,885.13 -	1,885.13	1,763.69	12/2018 -	07/2021	31(O) -	0/0
339	SAMBHU KI BHURJ SOLAR 250 MW - [N18000285]NTPC,RAJASTHAN , EPC	01/2020	1,522.71 -	1,522.71	437.60	09/2021 01/2022	01/2022	4(O) 0	0/0
340	SAMBHU KI BHURJ-II SOLAR 300MW - [N18000286]NTPC,RAJASTHAN , EPC	03/2020	1,782.00 -	1,782.00	200.75	09/2021 01/2022	01/2022	4(O) 0	0/0
341	JETSAR SOLAR 160 MW - [N18000287]NTPC,RAJASTHAN , EPC	12/2019	702.28 -	702.28	.00	03/2021 -	-	-	0/0
342	FATEHGARH SOLAR 296MW - [N18000289]NTPC,RAJASTHAN , EPC	03/2020	1,749.31 -	1,749.31	.00	09/2021 -	09/2021	0(O) -	0/0
343	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU , Central Sector Projects	05/2017	186.17 219.66	219.66	157.20	07/2019 04/2021	06/2021	23(O) 2	0/0
344	ETTAYAPURAM SOLAR 230MW - [N18000290]NTPC,TAMIL NADU , EPC	03/2020	1,316.22 -	1,316.22	.00	09/2021 -	09/2021	0(O) -	0/0
345	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA ,	01/2016	10,598.98 10,997.70	10,997.70	8,368.64	11/2020 07/2022	07/2022	20(O) 0	27/29
346	RAMAGUNDAM FLOATING SOLAR 100 MW - [N18000284]NTPC,TELANGANA , EPC	06/2019	401.90 -	401.90	.00	04/2021 -	04/2021	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
347	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH ,	09/2014	9,188.98 -	9,842.02	7,391.78	07/2019 03/2021	03/2021	-	42/42
348	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH , Joint Venture	04/2012	9,750.89 -	12,176.28	11,130.00	02/2017 -	01/2021	-	40/40
349	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH ,	03/2019	11,089.42 -	11,089.42	1,767.11	09/2023 -	08/2024	11(O) -	1/11
350	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000273]NTPC,UTTAR PRADESH ,	12/2018	587.44 -	587.44	463.48	09/2020 -	01/2021	-	0/0
351	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000274]NTPC,UTTAR PRADESH ,	03/2019	349.00 -	349.00	226.00	11/2020 -	04/2021	5(O) -	0/0
352	DEVIKOT SOLAR 90MW - [N18000280]NTPC,UTTAR PRADESH , EPC	03/2020	501.29 -	501.29	118.11	09/2021 01/2022	01/2022	4(O) 0	0/0
353	DEVIKOT SOLAR 150MW - [N18000281]NTPC,UTTAR PRADESH , EPC	01/2020	798.24 -	798.24	34.64	09/2021 01/2022	01/2022	4(O) 0	0/0
354	NOKHRA - [N18000282]NTPC,UTTAR PRADESH , EPC	03/2020	1,722.14 -	1,722.14	132.85	09/2021 01/2022	01/2022	4(O) 0	0/0
355	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND ,	11/2006	2,978.48 5,867.38	5,867.38	4,913.02	03/2013 12/2021	12/2022	117(O) 0	8/15
356	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND ,	08/2008	2,491.58 -	3,860.35	2,223.06	06/2013 -	12/2023	126(O) -	11/17
357	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND ,	07/2012	1,527.00 -	1,801.07	149.21	08/2017 -	-	-	0/15
358	NAITWAR MORI HEP - [N18000265]SJVN,UTTARAKHAND ,	10/2017	648.33 -	947.89	577.17	12/2021 -	12/2021	0(O) -	11/32
359	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL ,	09/2014	1,381.84 -	1,381.54	668.04	09/2019 12/2024	12/2024	63(O) 0	6/10
360	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL ,	04/2016	454.11 -	454.11	343.81	04/2018 03/2021	05/2021	37(O) 1	0/0
361	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC,WEST BENGAL ,	12/2016	529.68 -	529.68	418.49	11/2018 -	07/2021	32(O) -	0/0
	Total		2,95,137.42 -	3,67,699.63	2,56,834.13				619/756
	<u>HEAVY INDUSTRY</u>								
362	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL,DELHI , Central Sector Projects	08/2016	1,554.00 -	900.00	815.00	09/2019 -	-	-	0/0
	Total		1,554.00 -	900.00	815.00				0/0
	<u>HEALTH AND FAMILY WELFARE</u>								
363	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS-MNAGLAGIRI GUNTUR ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH , Central Sector Projects	08/2017	272.19 -	272.54	272.54	03/2019 -	03/2021	-	0/0
364	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH , Central Sector Projects	03/2018	601.02 -	601.02	400.25	- -	06/2021	- -	0/0
365	LGBRIMH-TEZPUR ASSAM - [N21000007]HSCC,ASSAM ,	07/2012	175.57 -	175.57	163.37	12/2014 -	03/2018	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
366	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI ASSAM - [N21000027]HITES,ASSAM ,	05/2017	875.00 -	747.80	331.55	05/2021 -	07/2022	14(O) -	0/0
367	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI ,	02/2013	414.11 -	499.23	494.72	11/2013 -	05/2021	90(O) -	0/0
368	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI ,	12/2013	204.44 -	250.00	240.24	05/2017 -	03/2021	-	2/2
369	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI ,	08/2014	293.65 -	325.00	299.76	05/2017 -	01/2020	-	5/5
370	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI ,	12/2017	156.56 -	190.34	143.14	- -	06/2021	- -	0/0
371	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA , Central Sector Projects	01/2018	249.01 -	249.07	231.05	- -	01/2021	-	0/0
372	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA ,	09/2014	505.58 -	585.00	586.96	03/2018 -	09/2019	-	2/2
373	AIIMS BILASPUR - [N21000028]NBCC,HIMACHAL PRADESH ,	04/2018	1,351.00 -	1,471.00	712.04	09/2021 -	09/2021	0(O) -	2/4
374	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD,HIMACHAL PRADESH ,	12/2018	260.00 -	260.00	25.38	06/2021 -	05/2022	11(O) -	0/0
375	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR SAMBA JAMMU AND KASHMIR - [N21000029]CPWD,JAMMU AND KASHMIR ,	03/2019	1,404.00 -	1,404.00	200.58	09/2023 -	09/2023	0(O) -	0/0
376	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]CPWD,JAMMU AND KASHMIR ,	03/2019	1,577.00 -	1,828.00	.00	09/2025 -	09/2025	0(O) -	0/0
377	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150]CPWD,JAMMU AND KASHMIR ,	03/2019	1,828.00 -	1,828.00	.00	09/2025 -	05/2024	-16(O) -	0/0
378	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST - [N28000112]CPWD,KERALA ,	09/2017	150.29 -	150.29	43.43	03/2020 -	12/2021	21(O) -	2/7
379	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA , Central Sector Projects	08/2017	274.19 -	274.19	256.37	03/2019 -	01/2021	-	0/0
380	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA , Central Sector Projects	03/2018	582.99 -	582.99	482.32	- -	06/2021	- -	0/0
381	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA ,	10/2016	363.99 -	363.99	239.89	05/2018 -	12/2021	43(O) -	0/0
382	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT - [N28000139]CPWD,PONDICHERRY ,	03/2018	195.00 -	195.00	16.41	09/2020 -	04/2022	19(O) -	0/33
383	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB ,	07/2016	152.95 -	177.92	164.17	02/2018 -	03/2021	-	1/1
384	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA PUNJAB - [N21000026]HITES,PUNJAB ,	07/2016	703.00 -	557.48	469.13	06/2020 -	07/2021	13(O) -	0/0
385	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA ,	10/2016	209.84 -	209.84	136.48	03/2020 -	05/2021	14(O) -	1/5

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
386	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH , Central Sector Projects	03/2018	268.84 -	268.84	243.92	- -	03/2021	-	0/0
387	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH ,	07/2016	785.00 -	715.06	548.39	04/2020 -	07/2021	15(O) -	0/0
388	CONSTRUCTION OF HOSPITAL BLOCK IIT KHARAGPUR - [N21000010]HSCC, WEST BENGAL ,	12/2014	168.90 -	191.20	169.51	05/2017 -	07/2019	-	3/3
389	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC, WEST BENGAL ,	08/2016	244.00 -	248.00	224.92	09/2018 -	05/2019	-	0/0
390	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS KALYANI WEST BENGAL - [N21000018]HSCC, WEST BENGAL , Central Sector Projects	08/2017	355.15 -	355.15	298.76	03/2019 -	06/2021	27(O) -	0/0
391	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC, WEST BENGAL ,	04/2018	651.99 -	651.99	503.55	- -	06/2021	- -	0/0
	Total		15,273.26 -	15,628.51	7,898.83				18/62
	<u>RAILWAYS</u>								
392	NANDYAL-YERRAGUNTLA(NL) SCR - [220100192]SCR, ANDHRA PRADESH ,	03/1996	164.36 -	1,050.00	999.64	02/2009 -	-	-	0/0
393	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR, ANDHRA PRADESH ,	12/2001	1,045.20 -	2,120.16	883.52	03/2009 -	03/2024	180(O) -	0/0
394	GUDUR-DURGARA JAPATNAM - [N22000265]SCR, ANDHRA PRADESH ,	04/2011	761.37 -	761.37	.52	- -	-	-	0/0
395	CUMBUM-PRODDATUR - [N22000282]SCR, ANDHRA PRADESH ,	04/2013	829.00 -	829.00	.94	- -	-	-	1/1
396	NADIKUDE-SRI KALAHASTI - [N22000286]SCR, ANDHRA PRADESH ,	04/2011	2,288.70 -	2,643.25	1,231.85	03/2021 -	03/2024	36(O) -	0/1
397	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL, ANDHRA PRADESH ,	03/2012	1,503.71 -	3,377.00	2,683.67	03/2020 -	03/2022	24(O) -	0/0
398	DUVVADA-VIJAYAWADA - [N22000366]SCR, ANDHRA PRADESH ,	04/2015	3,873.07 -	3,873.07	.38	- -	-	-	0/0
399	GUNTUR-GUNTAKAL - [N22000368]SCR, ANDHRA PRADESH ,	04/2016	3,631.00 -	3,887.48	1,144.64	03/2022 -	03/2024	24(O) -	0/0
400	VIJAYAWADA-GUDUR - [N22000369]RVNL, ANDHRA PRADESH ,	04/2015	3,246.26 -	3,548.68	2,224.17	12/2023 -	12/2023	0(O) -	0/0
401	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR, ANDHRA PRADESH ,	04/2015	2,499.71 -	2,499.71	671.08	03/2022 03/2024	03/2024	24(O) 0	0/0
402	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI, ANDHRA PRADESH ,	01/2013	387.70 -	487.13	434.63	03/2018 -	03/2021	-	0/0
403	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI, ANDHRA PRADESH ,	08/2016	234.50 -	235.00	14.14	03/2019 -	-	-	0/0
404	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT) NEFR - [N22000086]NFR, ASSAM ,	09/2006	385.20 -	1,043.00	837.67	03/2019 -	03/2023	48(O) -	0/0
405	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR, ASSAM ,	04/2011	314.00 486.96	800.00	823.02	03/2019 -	03/2021	-	0/0
406	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR, ASSAM ,	04/2015	2,232.32 -	2,950.00	1,620.12	03/2022 -	03/2023	12(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
407	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM ,	04/2015	870.96 -	1,873.21	1,309.41	03/2021 -	05/2021	2(O) -	0/0
408	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC) ECR - [220100240]ECR,BIHAR ,	04/1997	324.73 -	1,070.00	1,069.58	03/2012 -	11/2022	128(O) -	0/0
409	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR ,	04/1997	162.87 -	614.45	348.95	-	12/2023	-	0/0
410	HAJIPUR-SUGAULI VIA VAISHALI (NL) ECR - [220100303]ECR,BIHAR ,	04/2003	528.65 -	2,066.78	1,560.44	-	03/2023	-	0/0
411	KOSI BRIDGE (NL) ECR - [220100304]ECR,BIHAR ,	04/2002	499.41 -	516.02	447.86	03/2020 -	-	-	0/0
412	DANIAWAN-BIHARSARIF (NL) ECR - [220100311]ECR,BIHAR ,	04/2001	406.92 -	339.00	200.00	-	-	-	0/0
413	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR ,	04/1996	477.88 283.95	751.55	694.88	03/2012 -	07/2021	112(O) -	0/0
414	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) NEFR - [N22000087]NFR,BIHAR ,	09/2006	532.87 2,132.03	2,145.00	1,001.65	03/2019 -	03/2024	60(O) -	0/0
415	KISHANGANJ JALALGARH NL NEFR - [N22000101]NFR,BIHAR ,	04/2008	333.76 -	360.00	6.74	-	-	-	0/0
416	ARA-BHABHUA ROAD (NL) - [N22000166]ECR,BIHAR ,	04/2008	633.87 -	633.87	.40	-	-	-	0/0
417	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR ,	04/2008	620.57 -	620.57	.31	-	-	-	0/0
418	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR ,	04/2008	445.25 -	445.25	1.15	-	-	-	0/0
419	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR ,	04/2008	326.20 -	2,995.01	2.08	-	03/2024	-	0/0
420	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR ,	04/1999	325.00 -	735.20	384.25	-	03/2021	-	0/0
421	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR ,	04/2006	378.56 -	1,858.75	386.35	-	03/2023	-	0/0
422	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR ,	04/2005	205.00 -	205.00	5.21	-	-	-	0/0
423	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR ,	04/2006	211.00 -	1,006.00	24.16	-	-	-	0/0
424	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR ,	04/2008	678.62 -	678.62	17.20	-	-	-	0/0
425	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR ,	04/2008	228.05 -	228.05	1.53	-	03/2024	-	0/0
426	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR ,	04/2008	1,605.17 -	1,605.17	53.52	-	03/2023	-	0/0
427	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR ,	04/2008	192.56 -	192.56	.39	-	-	-	0/0
428	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR ,	04/2008	281.30 -	281.30	.60	-	-	-	0/0
429	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR ,	04/2004	372.14 -	1,470.50	1,288.24	-	03/2023	-	0/0
430	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR ,	04/2009	548.00 -	819.01	535.44	03/2020 -	03/2023	36(O) -	0/0
431	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR ,	04/2013	213.01 -	480.00	486.66	-	-	-	0/1

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
432	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR ,	05/2015	380.00 -	519.33	282.65	- -	03/2025	- -	0/0
433	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR ,	12/2015	1,200.20 1,200.20	1,200.20	578.18	03/2020 -	03/2023	36(O) -	0/1
434	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR ,	12/2015	1,491.47 -	1,491.47	508.88	03/2020 -	03/2023	36(O) -	1/1
435	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR ,	01/1991	332.15 -	546.71	541.43	07/2014 -	-	-	0/0
436	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR ,	04/2016	744.04 -	1,215.54	426.72	03/2021 -	03/2024	36(O) -	0/0
437	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR ,	04/2016	731.64 -	1,185.73	217.95	03/2021 -	06/2022	15(O) -	0/0
438	RAJGIR HISUA TALAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR,BIHAR ,	04/1998	180.82 -	726.31	546.29	- -	-	-	0/0
439	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA DANIYAWAN-BIHARSHARIF - [N22000476]ECR,BIHAR ,	04/1991	329.39 -	1,483.14	1,207.52	- -	03/2022	- -	0/0
440	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH ,	12/2012	1,160.00 1,160.83	1,160.83	950.18	03/2020 03/2023	03/2023	36(O) 0	1/1
441	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH ,	03/2007	1,402.02 -	1,300.00	1,294.72	03/2020 -	12/2021	21(O) -	0/0
442	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH ,	05/2014	207.00 -	207.00	153.83	03/2018 -	-	-	0/0
443	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR,CHHATISGARH ,	04/2008	872.00 -	1,226.51	1,131.91	12/2019 -	-	-	0/0
444	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATISGARH ,	04/2015	1,973.00 -	2,135.34	351.35	03/2021 -	12/2023	33(O) -	0/1
445	GEVRA ROAD PENDRA ROAD - [N22000488]IRCON,CHHATISGARH ,	02/2014	2,288.00 -	4,970.11	866.16	03/2022 -	12/2023	21(O) -	0/1
446	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON,CHHATISGARH ,	04/2013	3,055.00 -	3,055.15	2,431.72	09/2018 -	03/2022	42(O) -	0/1
447	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498]RITES,CHHATISGARH ,	02/2016	393.98 -	393.98	350.81	03/2020 -	06/2021	15(O) -	1/2
448	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI ,	04/1999	156.65 -	359.00	111.51	- -	03/2024	- -	0/0
449	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI ,	04/2012	295.68 -	419.00	127.91	- -	09/2023	- -	0/0
450	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT ,	04/2008	829.74 1,959.74	1,959.74	1,799.00	03/2020 03/2024	03/2024	48(O) 3	0/0
451	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT ,	04/2008	318.24 411.62	411.62	126.05	03/2012 03/2023	03/2023	132(O) 0	0/0
452	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT ,	04/2006	117.36 196.95	202.35	809.40	03/2011 -	-	-	0/0
453	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT ,	04/2012	975.62 -	1,500.00	1,497.74	12/2021 -	12/2021	0(O) -	0/0
454	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT ,	04/2012	644.38 -	872.65	800.30	03/2021 -	03/2021	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
455	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT ,	04/2011	844.10 844.10	844.10	186.59	- 03/2024	03/2024	- 0	0/0
456	RAJKOT-VERAVAL WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT ,	04/1994	320.66 1,378.11	1,378.11	540.09	03/2019 03/2023	03/2023	48(O) 0	0/0
457	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT ,	04/2013	1,548.66 -	1,868.89	1,831.45	12/2021 -	03/2022	3(O) -	0/0
458	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT ,	04/2011	1,037.15 1,389.05	1,389.05	1,125.73	03/2021 12/2021	12/2021	9(O) 0	0/0
459	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT ,	04/2015	1,002.39 1,002.39	1,002.39	653.86	03/2021 12/2022	12/2022	21(O) 0	0/0
460	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT ,	10/2013	343.00 -	343.00	222.83	03/2019 -	-	-	0/0
461	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT ,	03/2017	243.60 -	243.60	.00	- -	-	-	0/0
462	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT ,	03/2012	248.26 -	248.26	.00	- -	-	-	0/0
463	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT ,	03/2012	153.83 -	153.83	.00	- -	-	-	0/0
464	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT ,	02/1991	551.51 890.76	890.76	745.11	03/2019 10/2021	10/2021	31(O) 0	0/0
465	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT ,	04/2017	691.84 1,017.91	1,017.91	719.56	03/2020 02/2021	02/2021	-	0/0
466	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA ,	04/2012	287.00 -	893.45	705.53	12/2011 -	06/2021	114(O) -	0/0
467	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA ,	12/2015	346.32 -	346.32	320.28	03/2019 -	03/2021	-	0/0
468	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH ,	04/2008	2,966.99 -	6,753.42	926.84	12/2026 -	12/2025	-12(O) -	0/0
469	UDHAMPUR-SRINAGAR-BARAMULLA (NL) NR - [220100133]NR,JAMMU AND KASHMIR ,	03/1995	2,500.00 -	27,949.00	24,040.61	11/2002 -	12/2022	241(O) -	0/0
470	KODERMA-RANCHI VIA BARKAKANA (NL) ECR - [220100222]ECR,JHARKHAND ,	03/1999	1,033.07 -	3,550.00	3,567.20	- -	03/2022	- -	0/0
471	KODERMA-TILAIYA (NL) ECR - [220100305]ECR,JHARKHAND ,	04/2002	459.91 -	1,625.87	758.44	- -	03/2023	- -	0/0
472	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND ,	04/2012	258.20 358.68	358.68	314.33	12/2018 12/2018	04/2021	28(O) -2	0/0
473	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND ,	04/2012	148.77 -	377.00	201.09	12/2016 -	08/2020	-	0/0
474	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND ,	03/2016	1,724.20 -	1,724.20	839.51	03/2021 03/2021	12/2023	33(O) 0	0/0
475	GARHWA ROAD-RAMNA - [N22000465]ECR,JHARKHAND ,	03/2015	348.23 -	348.23	336.32	03/2021 -	03/2022	12(O) -	0/0
476	HUBLI-ANKOLA(NL) SWR - [220100193]SWR,KARNATAKA ,	04/1997	2,315.00 -	3,911.65	157.01	- -	12/2024	- -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
477	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA ,	04/1996	1,382.78 -	1,382.78	7.35	03/2002 -	03/2024	264(O) -	0/0
478	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA ,	04/2011	1,801.01 -	1,967.00	71.56	- -	12/2023	- -	0/0
479	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA ,	04/2010	986.30 -	986.30	312.23	03/2016 -	12/2023	93(O) -	1/1
480	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA ,	04/2013	558.00 -	558.00	.00	- -	12/2023	- -	0/0
481	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA ,	04/2011	832.47 -	832.47	.94	03/2016 -	03/2024	96(O) -	0/0
482	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA ,	04/2011	348.85 -	348.85	.36	- -	12/2023	- -	0/0
483	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA ,	04/2010	2,127.00 -	3,000.00	2,208.46	03/2023 -	12/2022	-3(O) -	0/1
484	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA ,	04/2011	146.75 -	167.50	.34	- -	12/2023	- -	0/0
485	GADAG-WADI NL - [N22000299]SWR,KARNATAKA ,	04/2013	2,841.84 -	2,841.84	304.83	12/2018 -	06/2025	78(O) -	0/0
486	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA ,	04/2013	327.25 -	327.25	.00	- -	12/2023	- -	0/0
487	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA ,	04/2012	279.54 -	279.54	35.29	03/2016 -	12/2023	93(O) -	0/0
488	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA ,	03/2015	1,156.94 -	1,656.00	1,160.49	03/2020 03/2023	03/2023	36(O) 16	1/5
489	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA ,	03/2015	578.00 -	783.00	620.29	03/2020 06/2021	06/2021	15(O) 0	1/2
490	KADUR CHIKMAGALUR SAKLSEHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA ,	03/1996	644.78 -	998.00	463.45	03/2017 03/2025	03/2025	96(O) 0	0/0
491	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA ,	10/1998	1,566.00 -	2,815.62	262.68	- -	-	-	0/0
492	KUMBALAM-TURAVUR - [N22000191]SR,KERALA ,	04/2011	252.96 -	369.55	8.50	- -	-	-	0/0
493	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA ,	04/2010	189.24 -	275.21	6.73	- -	-	-	0/0
494	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA ,	02/2015	1,431.90 -	1,431.90	198.81	- -	-	-	0/0
495	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA ,	02/2015	1,000.00 -	1,246.00	.81	- -	-	-	0/0
496	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA ,	02/2012	550.00 -	550.00	.00	03/2016 -	-	-	0/0
497	RAMGANJMUNDI-BHOPAL (NL) WCR - [220100314]WCR,MADHYA PRADESH ,	04/2001	424.60 -	2,909.99	1,229.79	03/2021 03/2029	03/2023	24(O) 0	4/15
498	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH ,	04/2005	383.79 -	1,413.76	1,416.77	- -	-	-	0/0
499	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH ,	04/2008	3,503.69 5,912.40	5,912.40	2,161.74	03/2022 03/2024	03/2024	24(O) 0	0/0
500	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH ,	12/2015	1,763.93 -	1,762.94	1,156.42	03/2020 -	03/2024	48(O) -	1/1
501	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH ,	04/2011	1,485.85 -	1,835.83	1,571.35	12/2020 -	12/2021	12(O) -	0/0
502	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH ,	06/2016	2,478.23 -	2,478.23	477.93	03/2022 -	03/2023	12(O) -	0/10

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
503	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH ,	08/2016	582.13 1,247.64	1,247.64	296.69	03/2022 -	03/2023	12(O) -	1/1
504	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH ,	12/2015	174.00 -	174.00	172.08	03/2019 -	-	-	0/0
505	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH ,	04/2010	585.93 -	1,268.32	941.56	02/2019 -	12/2021	34(O) -	0/1
506	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH ,	04/2015	1,370.00 -	1,370.94	470.49	12/2021 -	12/2023	24(O) -	0/0
507	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH ,	04/2016	700.00 603.69	603.69	254.73	06/2020 03/2023	03/2023	33(O) 0	0/0
508	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA ,	03/1996	495.44 -	2,980.41	1,768.25	03/2004 -	03/2022	216(O) -	0/0
509	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA ,	02/1997	2,271.50 -	4,517.49	2,648.51	03/2021 -	03/2023	24(O) -	0/0
510	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA ,	04/2008	5,300.00 -	918.53	284.75	03/2014 -	-	-	0/0
511	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA ,	04/2012	714.10 -	714.10	65.20	04/2016 -	-	-	0/0
512	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA ,	04/2008	3,168.29 -	3,168.29	1,352.27	03/2023 -	03/2023	0(O) -	0/0
513	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA ,	04/2011	792.89 -	1,377.48	335.23	03/2021 -	03/2023	24(O) -	0/0
514	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA ,	04/2011	184.06 -	315.00	312.62	03/2019 -	-	-	0/0
515	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA ,	04/2012	540.02 -	540.02	272.55	03/2022 -	03/2024	24(O) -	0/0
516	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA ,	02/2016	9,968.00 -	9,968.00	.00	03/2024 -	03/2024	0(O) -	0/0
517	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA ,	02/2016	2,425.00 -	5,341.68	.00	03/2024 -	03/2024	0(O) -	0/0
518	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA ,	02/2016	2,750.00 -	3,438.51	.00	03/2024 -	03/2024	0(O) -	0/0
519	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA ,	02/2015	1,272.19 -	1,283.49	408.70	03/2022 -	03/2023	12(O) -	0/0
520	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA ,	02/2015	2,449.91 -	2,449.91	332.19	03/2023 -	03/2024	12(O) -	0/0
521	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA ,	02/2015	3,627.47 3,627.00	3,627.47	1,204.21	03/2024 -	03/2023	-12(O) -	0/0
522	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA ,	02/2016	1,876.00 -	2,081.27	445.15	03/2023 -	03/2023	0(O) -	0/0
523	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA ,	02/2016	1,035.16 -	1,035.16	244.12	03/2022 -	03/2024	24(O) -	0/0
524	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA ,	02/2016	637.95 -	637.95	182.65	03/2023 -	03/2024	12(O) -	0/0
525	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA ,	03/2009	713.48 -	2,725.00	2,554.71	03/2020 -	12/2021	21(O) -	0/0
526	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA ,	04/2015	723.78 -	723.78	.19	12/2025 -	03/2025	-9(O) -	0/0
527	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA ,	09/2016	1,908.51 -	3,524.81	982.38	03/2023 -	12/2023	9(O) -	0/1

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
528	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA ,	10/2013	305.00 -	305.00	269.73	03/2019 -	12/2020	-	0/0
529	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA ,	03/2010	265.88 -	265.88	.00	- -	-	-	0/0
530	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA ,	03/2012	217.38 -	217.38	.00	- -	-	-	0/0
531	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA ,	06/2018	229.00 -	1,096.00	39.79	12/2021 -	12/2024	36(O) -	0/1
532	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR ,	04/2003	4,454.17 -	12,264.15	10,994.55	03/2011 -	12/2023	153(O) -	0/0
533	NEW BG LINE FROM BYRNihat TO SHILLONG - [N22000205]NFR,MEGHALAYA ,	04/2010	906.46 1,202.33	4,083.02	264.33	03/2021 -	-	-	0/0
534	BHAIRABI SAIRONG NL NEFR - [N22000100]NFR,MIZORAM ,	04/2008	2,393.47 5,021.45	5,521.45	3,954.28	03/2014 -	03/2023	108(O) -	0/0
535	GONDIA-JABALPUR(GC) (SECR) - [220100186]SECR,MULTI STATE ,	02/1997	511.86 -	2,005.25	1,777.22	04/2020 -	04/2021	12(O) -	0/1
536	NANGALDAM-TALWARA(NL) NR - [220100188]NR,MULTI STATE ,	03/1981	450.00 -	2,200.00	714.78	07/2012 -	03/2024	140(O) -	0/0
537	MUNEERABAD-MAHABOBNAGAR(NL) SCR - [220100205]SCR,MULTI STATE ,	04/1997	1,723.00 1.00	3,421.35	1,895.77	03/2000 -	03/2023	276(O) -	0/0
538	LALITPUR-SATNA-REWA-SINGRULI NL (NCR) - [220100232]WCR,MULTI STATE ,	09/1998	247.66 -	8,248.50	2,131.17	05/2008 -	03/2025	202(O) -	0/9
539	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) NEFR - [220100266]NFR,MULTI STATE ,	04/2000	1,180.19 2,531.34	4,541.38	3,804.55	12/2008 -	05/2021	149(O) -	0/0
540	DEOGHAR - SULTANGANJ (INL) ER - [220100273]ER,MULTI STATE ,	04/2000	607.09 -	1,425.44	638.05	02/2013 -	03/2024	133(O) -	0/0
541	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE ,	04/2005	230.03 -	230.03	277.14	12/2022 -	12/2022	0(O) -	0/0
542	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE ,	03/2007	243.78 -	895.00	111.89	12/2021 -	12/2021	0(O) -	0/0
543	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE ,	03/2013	295.00 -	477.31	378.98	01/2019 -	02/2022	37(O) -	0/0
544	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE ,	04/2007	1,347.26 1,347.26	1,347.26	907.54	03/2022 03/2023	03/2023	12(O) 0	0/0
545	DAHOD-INDORE VIA SARDARPUR JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE ,	04/2007	1,640.04 1,640.04	1,640.04	866.42	03/2022 03/2023	03/2023	12(O) -24	0/0
546	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE ,	04/2011	2,082.75 -	4,262.36	186.12	- -	-	-	0/1
547	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE ,	04/2011	2,912.96 -	3,845.60	148.26	03/2022 -	12/2024	33(O) -	0/3
548	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE ,	04/2010	2,030.50 -	2,030.50	19.07	- -	-	-	0/0
549	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE ,	04/2010	651.00 -	1,009.00	7.96	03/2015 -	03/2025	120(O) -	0/0
550	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE ,	04/2008	415.67 -	549.75	15.58	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above. (All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
551	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE ,	04/2013	1,798.00 2,042.51	2,042.51	136.41	03/2019 -	03/2024	60(O) -	0/0
552	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE ,	04/2008	523.52 -	1,205.00	2.28	- -	03/2024	- -	0/0
553	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE ,	04/2007	270.14 -	457.08	439.49	- -	12/2021	- -	0/0
554	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE ,	04/2010	242.22 -	471.00	76.56	03/2020 -	-	-	0/0
555	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE ,	04/2010	241.52 -	373.87	287.09	- -	12/2021	- -	0/0
556	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE ,	04/2011	414.84 -	1,040.00	156.54	03/2020 -	-	-	0/0
557	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE ,	04/1999	819.23 -	1,871.00	1,082.01	- -	-	-	0/0
558	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE ,	04/2011	120.70 -	2,172.16	262.36	03/2019 -	12/2027	105(O) -	0/0
559	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE ,	04/1987	406.99 -	545.70	149.31	03/2006 -	03/2025	228(O) -	0/0
560	SULTANGANJ-KATURIA VIA ASARGANJ TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE ,	04/2007	450.00 -	1,261.34	.00	- -	03/2025	- -	0/0
561	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE ,	04/2010	172.03 -	260.10	11.74	- -	03/2025	- -	0/0
562	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE ,	04/2013	915.98 -	2,137.81	388.53	03/2022 -	03/2025	36(O) -	0/0
563	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE ,	04/2011	288.35 -	502.48	432.62	- -	03/2021	-	0/0
564	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE ,	04/2011	261.38 -	565.00	547.01	- -	05/2019	-	0/0
565	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE ,	04/2001	923.52 -	995.10	645.97	03/2016 -	03/2025	108(O) -	0/0
566	CHINPAI-SAINTHIA DOUBLING MM FOR PRANTI-SURI CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE ,	04/2005	595.51 -	769.40	103.86	03/2017 -	03/2025	96(O) -	0/0
567	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE ,	04/2010	174.56 -	174.56	71.43	- -	03/2025	- -	0/0
568	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE ,	04/2010	277.28 -	266.32	191.22	03/2016 -	03/2025	108(O) -	0/0
569	DANKUNI-CHANDANPUR 4TH LINE 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE ,	04/2010	365.17 -	439.30	411.65	03/2017 -	03/2025	96(O) -	0/0
570	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE ,	04/2010	157.94 -	157.94	51.74	11/2018 -	03/2021	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
571	BARIARPIUR-MANANPURVIA KHARAGPUER LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE ,	04/2007	450.55 -	250.55	20.11	- -	03/2025	- -	0/0
572	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE ,	04/2010	365.17 -	527.54	1.76	- -	03/2025	- -	0/0
573	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE ,	04/2011	542.18 -	663.13	534.85	03/2020 -	03/2021	-	0/0
574	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE ,	04/2011	175.80 -	495.10	288.51	- -	03/2022	- -	0/0
575	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE ,	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	108(O) -	0/0
576	NEW ALIPUR TO AKRA MM FOR BUDGE BUDGE-PUJALI NL PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE ,	04/2010	494.54 -	494.59	32.00	03/2005 -	03/2025	240(O) -	0/0
577	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE ,	04/2000	297.47 -	298.22	52.09	- -	03/2025	- -	0/0
578	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE ,	04/2003	337.96 -	336.96	70.20	- -	03/2025	- -	0/0
579	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE ,	04/2009	499.96 -	680.68	164.09	02/2012 -	03/2025	157(O) -	0/0
580	LILUAH-DANKUNI 3RD LINE MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE ,	04/2009	257.42 -	257.42	107.35	03/2014 -	03/2025	132(O) -	0/0
581	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE ,	04/2011	166.89 -	166.89	.02	- -	03/2025	- -	0/0
582	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE ,	04/2012	1,856.95 -	1,952.68	567.51	03/2023 -	03/2024	12(O) -	0/0
583	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE ,	04/2007	336.91 -	791.39	572.99	- -	03/2023	- -	0/0
584	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE ,	04/2013	296.00 -	296.10	.01	- -	12/2023	- -	0/0
585	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE ,	04/2007	2,062.30 -	2,432.50	1,127.71	- -	03/2025	- -	2/2
586	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE ,	04/2010	704.31 -	927.94	534.34	03/2020 03/2022	06/2021	15(O) 0	1/1
587	KADAPA-BANGALORE (NL) KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE ,	04/2008	2,132.77 -	3,037.95	350.54	03/2014 -	03/2027	156(O) -	1/1
588	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE ,	04/2012	250.93 -	310.70	293.10	- -	03/2024	- -	0/0
589	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE ,	05/2015	600.00 -	701.81	236.13	03/2020 -	10/2022	31(O) -	0/0
590	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE ,	05/2015	860.43 -	1,147.00	911.86	03/2020 -	06/2021	15(O) -	0/0
591	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE ,	03/2015	1,614.59 -	1,870.41	1,341.15	03/2019 03/2024	03/2024	60(O) 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
592	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE ,	05/2015	678.54 678.54	929.86	848.39	03/2019 -	05/2021	26(O) -	0/38
593	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE , Central Sector Projects	10/2006	11,589.00 30,357.00	28,181.00	.00	- -	-	-	0/0
594	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE ,	04/2015	2,063.03 -	2,063.03	1,416.78	03/2021 -	03/2024	36(O) -	0/0
595	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE ,	04/2015	636.38 -	636.38	.00	- -	-	-	0/0
596	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE ,	12/2015	1,08,000.00 -	1,08,000.00	12,039.69	12/2023 -	12/2023	0(O) -	0/0
597	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE ,	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	-	-	0/0
598	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE ,	04/2007	328.14 1,540.13	1,540.13	242.04	03/2023 03/2025	03/2025	24(O) 0	0/0
599	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE ,	03/2002	625.00 -	859.00	852.73	03/2016 -	06/2021	63(O) -	0/0
600	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND ,	04/2006	2,326.52 -	6,911.00	1,204.64	03/2015 -	12/2024	117(O) -	0/0
601	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND ,	04/2013	4,274.00 -	4,274.00	.00	03/2020 -	-	-	0/0
602	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA ,	04/1994	2,923.13 3,791.66	3,791.66	1,506.95	03/2009 03/2026	03/2026	204(O) 0	0/0
603	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA ,	04/1996	1,185.64 -	1,844.47	1,883.44	12/2017 -	-	-	0/0
604	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA ,	04/1998	1,202.70 -	2,440.53	1,337.54	02/2015 -	06/2022	88(O) -	0/0
605	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA ,	04/2000	133.41 207.00	396.00	388.21	03/2009 03/2009	-	-	1/1
606	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA ,	04/2005	810.78 1,928.07	1,928.07	873.81	06/2021 03/2025	03/2025	45(O) 0	0/0
607	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA ,	04/2010	149.90 -	230.00	54.46	03/2015 -	-	-	0/0
608	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA ,	03/2011	1,111.99 -	1,539.28	1,109.06	02/2019 -	12/2021	34(O) -	0/0
609	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA ,	03/2013	843.04 843.04	843.04	227.52	10/2020 03/2024	03/2024	41(O) 0	0/0
610	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA ,	03/2012	155.81 238.03	238.03	221.48	03/2020 03/2021	03/2022	24(O) 0	0/0
611	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA ,	04/2015	1,547.38 1,547.38	1,547.38	612.77	03/2022 03/2023	03/2023	12(O) 0	0/0
612	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA ,	04/2015	2,361.74 2,361.74	2,361.74	432.17	03/2022 03/2026	03/2026	48(O) 0	0/0
613	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA ,	04/2015	701.61 -	810.02	171.45	11/2018 -	03/2024	64(O) -	0/0
614	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA ,	04/2015	1,172.92 1,172.92	1,172.92	613.52	12/2018 03/2024	03/2024	63(O) 0	0/0
615	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA ,	11/2015	969.83 1,312.96	1,312.96	940.00	03/2020 03/2020	12/2021	21(O) 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
616	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA ,	01/1991	2,335.67 -	3,327.72	1,317.36	12/2024 -	12/2026	24(O) -	0/0
617	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA ,	03/2006	948.04 -	2,009.00	1,875.48	03/2020 -	12/2021	21(O) -	0/0
618	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA ,	03/2009	942.95 -	1,536.00	1,089.84	03/2019 -	06/2022	39(O) -	0/0
619	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA ,	04/2016	5,200.00 -	962.00	54.75	03/2020 -	03/2024	48(O) -	0/0
620	QADIAN-BEAS - [N22000295]NR,PUNJAB ,	04/2011	205.22 -	841.90	1.73	- -	03/2024	- -	0/0
621	MANSA-BHATINDA (PHASE-I) INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI - [N22000502]NR,PUNJAB ,	06/2009	404.00 -	404.00	226.25	08/2016 -	08/2025	108(O) -	0/0
622	DAUSA-GANGAPUR CITY(NL) NWR - [220100184]NWR,RAJASTHAN ,	02/1997	410.08 -	860.41	709.62	02/2019 -	06/2022	40(O) -	0/0
623	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN ,	04/2012	246.08 -	395.00	348.47	12/2019 -	02/2021	-	0/0
624	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN ,	04/2013	236.93 -	350.45	273.79	10/2018 -	01/2020	-	0/0
625	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN ,	04/2013	822.00 -	1,099.00	.00	- -	-	-	0/1
626	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN ,	04/2013	323.00 -	432.22	.00	- -	-	-	0/0
627	MAVLI JUNCTION-BARI SADRI MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN ,	04/2013	420.18 -	480.00	357.41	03/2020 -	06/2021	15(O) -	0/0
628	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN ,	04/2011	213.39 -	375.00	348.55	11/2019 -	03/2021	-	0/0
629	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN ,	04/2013	242.09 -	525.00	460.83	02/2019 -	02/2020	-	0/0
630	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN ,	05/2015	873.71 -	1,980.21	4.60	- -	-	-	0/0
631	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN ,	01/2011	493.17 -	493.17	464.53	03/2018 -	-	-	0/0
632	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN ,	08/2018	808.85 -	808.85	232.42	08/2022 -	11/2022	3(O) -	0/0
633	SEVOK RANGPO NEFR - [N22000102]NFR,SIKKIM ,	04/2008	1,339.48 -	8,600.00	619.18	12/2015 -	-	-	0/0
634	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU ,	09/1995	303.98 -	1,720.00	701.37	03/2020 -	03/2025	60(O) -	0/0
635	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS MTP - [N22000028]MRTP,TAMIL NADU ,	04/2006	495.74 -	734.01	510.69	06/2013 06/2022	12/2021	102(O) 0	1/4
636	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU ,	09/2007	724.69 -	2,910.84	1,621.40	02/2019 -	03/2025	73(O) -	0/0
637	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU ,	09/2006	227.40 -	227.40	63.90	- -	-	-	0/0
638	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU ,	09/2006	582.83 -	582.83	239.49	- -	12/2025	- -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
639	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU ,	04/2008	151.84 -	527.37	2.59	02/2019 -	-	-	0/0
640	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU ,	04/2013	839.00 -	1,500.00	.63	- -	-	-	0/0
641	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU ,	04/1999	198.68 -	559.95	52.50	- -	03/2024	-	0/0
642	ERODE-PALANI - [N22000199]SR,TAMIL NADU ,	04/2008	288.57 -	1,140.00	1.63	- -	-	-	0/0
643	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU ,	04/2008	164.41 -	608.13	375.67	- 10/2021	09/2021	- 0	0/0
644	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU ,	04/2007	931.98 -	1,121.00	928.75	- 05/2021	05/2021	- 1	0/0
645	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU ,	10/2013	187.26 -	327.00	268.75	04/2014 -	12/2020	-	0/0
646	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU ,	02/1996	268.87 -	950.00	928.36	03/2005 -	09/2021	198(O) -	0/0
647	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU ,	02/1999	257.00 257.00	238.00	153.70	03/2018 -	-	-	0/0
648	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU ,	02/2017	1,567.00 -	1,567.00	.00	03/2024 -	03/2026	24(O) -	0/0
649	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU ,	02/2015	1,700.00 -	1,305.00	756.45	03/2022 -	06/2022	3(O) -	0/0
650	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU ,	02/2015	760.00 -	1,536.00	1,233.08	03/2020 -	06/2022	27(O) -	0/0
651	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA ,	04/2006	1,160.48 -	1,160.48	502.93	03/2010 -	03/2024	168(O) -	1/1
652	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA ,	04/2012	632.68 -	950.00	810.96	03/2016 -	12/2021	69(O) -	0/0
653	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA ,	04/2013	1,112.00 -	2,911.84	.92	- -	-	-	1/1
654	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES,TELANGANA ,	03/2015	636.38 -	636.38	581.85	03/2021 -	03/2021	-	3/3
655	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA ,	04/2015	773.94 -	850.00	705.50	12/2024 -	12/2024	0(O) -	0/0
656	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA ,	04/2017	119.73 185.00	449.39	7.09	03/2022 -	12/2022	9(O) -	0/0
657	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA ,	04/2012	569.63 -	742.00	200.28	03/2020 -	03/2022	24(O) -	2/3
658	ETAWAH-MAINPURI (NL) NCR - [220100318]NCR,UTTAR PRADESH ,	04/1997	120.00 -	346.00	345.51	12/2008 -	-	-	0/0
659	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH ,	02/2008	171.10 -	275.08	141.55	03/2012 -	-	-	0/0
660	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH ,	03/2013	307.00 -	1,409.09	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
661	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH ,	03/2013	643.00 -	644.00	.00	- -	-	-	0/0
662	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH ,	04/2012	1,229.00 -	1,265.00	103.72	- -	03/2023	-	0/0
663	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH ,	04/2014	182.92 -	197.73	.00	- -	-	-	0/0
664	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH ,	03/2015	1,295.42 -	1,295.42	1,111.50	03/2022 -	03/2022	0(O) -	0/0
665	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR,UTTAR PRADESH ,	04/2015	668.70 668.00	680.00	330.00	03/2020 -	-	-	4/6
666	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH ,	04/2015	943.60 -	1,000.00	688.03	03/2022 -	12/2024	33(O) -	0/0
667	LUCKNOW- PILIBHIT VIA SITAPUR LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH ,	04/2011	927.01 -	1,400.00	1,331.76	03/2019 -	06/2022	39(O) -	0/0
668	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH ,	04/2015	1,765.92 -	1,765.92	887.48	03/2023 -	12/2024	21(O) -	0/0
669	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH ,	03/2012	1,183.25 -	1,825.00	1,411.49	12/2020 -	12/2022	24(O) -	0/0
670	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH ,	08/2015	2,436.21 -	2,436.21	1,138.31	03/2020 -	03/2024	48(O) -	0/0
671	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH ,	08/2015	528.57 -	528.57	179.78	03/2019 -	03/2022	36(O) -	0/0
672	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH ,	04/2016	213.00 -	213.35	12.86	04/2016 -	12/2021	68(O) -	0/0
673	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH ,	04/2016	1,900.00 -	1,277.06	.00	01/2022 -	03/2025	38(O) -	0/0
674	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH ,	04/2017	150.00 -	150.00	.00	04/2017 -	10/2022	66(O) -	0/0
675	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH ,	04/2017	1,343.00 -	1,476.15	.00	01/2018 -	-	-	0/0
676	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH ,	04/2017	622.50 427.00	426.74	506.36	04/2017 -	03/2021	-	0/0
677	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH ,	04/2017	276.90 -	276.90	.00	04/2017 -	04/2022	60(O) -	0/0
678	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH ,	04/2016	602.50 -	714.34	40.34	- -	12/2023	-	0/0
679	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]NER,UTTAR PRADESH ,	04/2016	600.00 -	366.71	117.64	01/2022 -	03/2022	2(O) -	0/0
680	SHAHGANJ-BHATNI-PHEPHNA-INDARA MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH ,	04/2016	1,177.96 -	1,028.95	172.26	12/2019 -	04/2021	16(O) -	0/0
681	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH ,	03/2018	4,329.53 -	4,329.53	33.37	03/2023 -	03/2023	0(O) -	0/0
682	JHANSI BINA DOUBLING - [N22000496]NCR,UTTAR PRADESH ,	09/2016	2,001.00 -	2,001.00	809.66	03/2021 -	-	-	0/6
683	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501]RVNL,UTTAR PRADESH ,	06/2016	3,677.76 -	3,677.76	446.65	12/2023 -	12/2023	0(O) -	0/0
684	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND ,	04/2003	142.45 -	228.40	.15	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
685	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND ,	04/2012	219.83 -	346.63	204.53	- -	-	-	0/0
686	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND ,	04/2011	16,216.00 -	22,716.11	2,997.71	12/2024 -	03/2025	3(O) -	0/0
687	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL) NEFR - [220100135]NFR,WEST BENGAL ,	04/1983	297.32 200.34	614.00	275.06	03/2019 -	-	-	0/0
688	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL ,	04/1974	393.46 154.30	1,026.00	182.49	03/2007 03/2007	-	-	0/0
689	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL ,	03/2000	1,049.69 -	3,404.92	3,837.57	12/2006 -	-	-	0/0
690	TARAKESWAR - BISHNUPUR NEW BG LINE (NL) ER - [220100272]ER,WEST BENGAL ,	04/2000	1,188.91 -	1,619.48	905.06	03/2019 12/2009	03/2025	72(O) 0	0/0
691	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL ,	04/2007	1,106.62 -	1,091.59	990.33	12/2010 -	03/2025	171(O) -	7/7
692	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL,WEST BENGAL ,	04/2010	2,397.72 -	2,397.72	197.20	03/2016 -	-	-	0/0
693	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL ,	04/2010	2,298.42 -	2,733.86	40.46	03/2014 -	12/2025	141(O) -	0/0
694	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL ,	04/2010	3,951.98 -	4,259.48	2,734.83	03/2016 -	03/2025	108(O) -	0/0
695	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL ,	04/2010	2,913.51 -	4,639.00	1,119.31	03/2016 -	03/2025	108(O) -	0/0
696	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL ,	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	63(O) -	0/0
697	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL ,	04/2010	267.37 -	620.00	40.99	- -	03/2025	- -	0/0
698	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL ,	04/2010	221.42 -	380.00	38.20	- -	-	-	0/0
699	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP,WEST BENGAL ,	04/2009	573.78 -	268.52	.03	- -	03/2025	- -	0/0
700	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL ,	04/2012	255.64 -	272.20	261.26	- -	03/2022	- -	0/0
701	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR,WEST BENGAL ,	04/2016	602.27 -	2,144.78	921.83	12/2021 -	04/2021	-8(O) -	0/0
702	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL ,	04/1998	1,027.40 1,966.70	2,373.00	485.04	03/2003 -	03/2030	324(O) -	0/0
703	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]NFR,WEST BENGAL ,	02/1999	380.60 -	1,090.60	1,089.12	04/2010 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	Total		4,62,095.03 -	7,00,076.37	2,50,483.48				37/139
	<u>HUMAN RESOURCE DEVELOPMENT</u>								
704	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM A.P. - [N28000133]CPWD,ANDHRA PRADESH ,	02/2019	186.00 199.00	205.00	130.63	09/2020 -	-	-	3/7
705	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE - [N42000005]CPWD,ANDHRA PRADESH ,	02/2019	655.34 -	655.34	49.89	06/2020 -	-	-	0/110
706	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE YERPEDU MANDAL CHITTOOR DISTRICT - [N42000007]CPWD,ANDHRA PRADESH ,	09/2019	588.72 -	588.72	14.80	09/2022 -	01/2023	4(O) -	0/0
707	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR ,	02/2016	496.18 496.00	498.99	224.58	06/2017 -	10/2021	52(O) -	2/6
708	PERMANENT CAMPUS FOR IIM BODH GAYA - [N42000009]CPWD,BIHAR ,	09/2018	375.00 -	375.00	48.46	09/2020 -	11/2022	26(O) -	0/0
709	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA DURG CHHATTISGARH STAGE I PHASE I. - [N28000141]CPWD,CHHATTISGARH ,	03/2020	808.62 -	808.62	57.42	07/2022 -	07/2022	0(O) -	0/0
710	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM GOA. - [N42000002]CPWD,GOA ,	05/2019	303.90 -	303.90	17.00	03/2020 -	-	-	0/8
711	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH ,	11/2012	270.83 -	270.83	226.16	11/2014 -	-	-	2/8
712	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR - [N42000008]CPWD,HIMACHAL PRADESH ,	09/2018	392.51 -	392.51	38.44	06/2022 -	06/2022	0(O) -	0/0
713	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130]CPWD,JAMMU AND KASHMIR ,	03/2019	329.00 -	329.00	.00	07/2022 -	07/2022	0(O) -	0/0
714	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]CPWD,JAMMU AND KASHMIR ,	01/2018	676.00 -	676.00	.00	04/2023 -	04/2023	0(O) -	0/0
715	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND ,	09/2012	171.86 -	171.86	111.29	03/2016 -	06/2021	63(O) -	1/6
716	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY DHARWAD (PHASE 1A) - [N42000006]CPWD,KARNATAKA , EPC	07/2019	851.00 851.00	851.00	26.10	03/2022 -	09/2022	6(O) -	0/0
717	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA ,	01/2010	165.23 -	165.23	118.52	10/2012 -	-	-	1/8
718	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE KANJIKODE WEST DISTRICT PALAKKA - [N28000140]CPWD,KERALA , Central Sector Projects	07/2019	753.63 -	753.63	58.47	03/2021 -	06/2022	15(O) -	0/0
719	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY POWAI MUMBAI - [N28000117]CPWD,MAHARASHTRA ,	01/2018	223.37 -	223.37	61.35	07/2020 -	06/2021	11(O) -	4/14

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
720	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]RITES,MEGHALAYA ,	09/2013	484.32 -	626.26	.00	09/2014 -	-	-	0/0
721	STUDY IN INDIA - [N42000003]EDCIL,MULTI STATE ,	03/2018	150.00 -	150.00	.00	04/2018 -	-	-	0/0
722	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION - [N42000004]IITKGP,MULTI STATE ,	08/2018	418.00 -	418.00	110.00	03/2019 -	-	-	0/0
723	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD,ODISHA ,	01/2019	790.79 -	790.79	173.98	03/2022 -	06/2022	3(O) -	0/5
724	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR PUNJAB - [N28000102]CPWD,PUNJAB ,	08/2016	294.00 -	350.69	276.69	04/2019 -	05/2021	25(O) -	7/8
725	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR PUNJAB - [N28000120]CPWD,PUNJAB ,	01/2018	430.00 -	387.83	199.99	05/2020 -	02/2022	21(O) -	2/5
726	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR PUNJAB. - [N28000142]CPWD,PUNJAB ,	10/2019	348.24 -	348.24	18.71	05/2022 -	08/2022	3(O) -	1/7
727	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN ,	12/2016	549.31 -	559.47	458.38	07/2019 -	-	-	3/6
728	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH ,	11/2017	171.72 -	171.72	53.94	03/2020 -	06/2021	15(O) -	0/0
729	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED - [N28000146]CPWD,WEST BENGAL , EPC	03/2020	193.83 -	193.83	.45	06/2020 -	-	-	0/0
	Total		11,077.40 -	11,265.83	2,475.25				26/198
	HOME AFFAIRS								
730	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI ,	10/2013	1,219.21 -	2,000.00	906.04	10/2019 -	12/2021	26(O) -	1/7
731	BUILDING OF THE FORCE HEADQUARTER INCLUDING SECTOR HQR RAF - [N45000002]CPWD,DELHI , EPC	06/2019	277.35 -	277.35	10.60	07/2022 -	07/2022	0(O) -	0/0
732	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE- - [N28000147]CPWD,HARYANA , EPC	01/2020	166.98 167.00	166.98	.00	10/2023 -	10/2023	0(O) -	0/0
733	CONSTRUCTION OF SEPARATE FAMILY ACCOMMODATION (440 NOS.) (PHASE- C/O 336 NOS. TYPE- II QTRS 96 - [N45000001]CPWD,HARYANA ,	01/2020	166.98 -	166.98	.29	05/2022 -	05/2022	0(O) -	0/0
734	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL , Central Sector Projects	10/2014	162.88 238.00	238.00	171.19	04/2018 12/2021	12/2021	44(O) 0	5/6
	Total		1,993.40 -	2,849.31	1,088.12				6/13

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>RURAL DEVELOPMENT</u>								
735	CONSTRUCTION OF GRAMEEN VIKAS BHAWAN (2BASEMENTS+ GROUND+9 FLOORS) FOR MINISTRY OF RURAL DEVELOPMENT - [N28000132]CPWD,DELHI ,	11/2018	361.60 -	361.60	12.44	07/2021 -	07/2021	0(O) -	0/2
736	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA ,	03/2007	149.73 173.00	155.66	144.95	12/2015 -	10/2021	70(O) -	0/1
737	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA ,	12/2007	202.61 227.00	207.12	190.22	12/2016 -	10/2021	58(O) -	2/5
738	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA ,	10/2011	175.49 206.71	175.49	124.87	12/2016 -	12/2021	60(O) -	0/4
	Total		889.43 -	899.87	472.48				2/12
	<u>CULTURE DEVELOPMENT</u>								
739	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE SHILONG IN MEGHALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA ,	04/2014	151.33 -	151.33	148.33	09/2017 -	03/2021	-	12/15
	Total		151.33 -	151.33	148.33				12/15
	<u>DPIIT</u>								
740	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]IICC,DELHI ,	11/2017	4,773.00 -	5,178.00	2,557.37	12/2019 -	12/2021	24(O) -	0/0
741	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]DMIC,MULTI STATE ,	09/2011	12,579.09 -	13,812.30	8,915.05	09/2019 01/2014	07/2021	22(O) 0	0/0
	Total		17,352.09 -	18,990.30	11,472.42				0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
742	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS ,	03/2015	262.97 -	262.97	.00	10/2018 -	-	-	0/4
743	2 LANE WITH HARD SHOLDER REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS ,	03/2017	409.85 -	409.85	21.11	12/2017 -	-	-	0/4
744	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS ,	03/2015	277.17 -	277.17	159.49	04/2017 -	-	-	3/4
745	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS ,	02/2018	391.00 -	391.00	22.17	10/2018 -	-	-	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
746	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS ,	03/2018	234.27 -	234.27	11.03	10/2018 -	-	-	1/4
747	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MoRTH,A & N ISLANDS ,	11/2017	237.80 -	238.00	7.48	11/2019 -	-	-	0/0
748	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH,A & N ISLANDS ,	11/2017	257.34 -	238.00	41.09	11/2019 -	-	-	0/0
749	AJANTHA TO BULDHANA - [N24001008]MoRTH,A & N ISLANDS ,	02/2017	401.00 401.00	401.00	143.81	07/2019 -	-	-	0/4
750	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH , PPP (BOT)	04/2011	571.00 -	571.00	582.53	10/2013 -	-	-	0/0
751	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2011	1,535.00 -	1,535.00	3,278.00	05/2014 -	-	-	0/0
752	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]MoRTH,ANDHRA PRADESH ,	07/2015	333.21 333.21	333.21	256.11	12/2015 -	-	-	0/2
753	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]MoRTH,ANDHRA PRADESH , EPC	01/2014	195.45 -	195.45	.00	11/2014 -	-	-	0/4
754	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]MoRTH,ANDHRA PRADESH , EPC	03/2015	271.45 -	271.45	225.81	10/2015 -	03/2021	-	3/4
755	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]MoRTH,ANDHRA PRADESH ,	07/2015	333.21 -	333.21	256.11	12/2015 -	-	-	0/2
756	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]MoRTH,ANDHRA PRADESH , EPC	10/2015	333.21 -	353.89	256.11	11/2015 -	-	-	0/0
757	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH ,	01/2016	1,134.97 -	1,134.97	1,634.05	11/2018 -	-	-	0/0
758	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH ,	09/2014	1,684.00 -	1,684.00	54.13	02/2017 -	-	-	0/0
759	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH ,	03/2017	1,041.62 -	1,187.10	951.13	03/2020 -	-	-	0/0
760	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH ,	12/2017	328.67 -	328.67	234.49	- -	-	-	0/0
761	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH ,	12/2017	1,323.15 -	1,323.15	785.33	- -	07/2021	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
762	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE OF - [N24000720]NHAI,ANDHRA PRADESH ,	12/2017	357.00 -	357.00	.00	- -	-	-	0/0
763	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH ,	02/2018	1,959.00 -	1,959.00	1,211.72	- -	10/2021	-	0/0
764	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH ,	03/2018	1,532.62 -	2,499.00	761.73	03/2021 10/2021	04/2021	1(0) 0	2/4
765	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH ,	03/2018	1,550.98 -	1,550.98	1,401.00	- -	09/2021	-	0/0
766	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH ,	03/2018	565.09 -	565.09	601.35	- -	02/2021	-	0/0
767	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH ,	03/2018	314.43 -	314.43	85.61	- -	03/2022	-	0/0
768	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH ,	03/2018	557.30 -	557.30	351.02	- -	-	-	0/0
769	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]MoRTH,ANDHRA PRADESH ,	10/2015	333.21 -	355.89	315.57	12/2015 -	-	-	3/3
770	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929]MoRTH,ANDHRA PRADESH ,	09/2016	372.68 -	372.68	185.04	02/2017 06/2021	06/2021	52(0) 0	3/4
771	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO - [N24000930]MoRTH,ANDHRA PRADESH ,	11/2016	378.24 -	378.24	315.42	01/2018 -	-	-	4/4
772	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931]MoRTH,ANDHRA PRADESH ,	11/2016	290.15 -	290.15	73.11	05/2017 07/2021	07/2021	50(0) 0	2/4
773	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932]MoRTH,ANDHRA PRADESH ,	01/2017	319.28 -	319.28	214.00	08/2017 -	08/2019	-	2/4
774	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]MoRTH,ANDHRA PRADESH ,	02/2017	429.43 -	429.43	256.15	11/2017 04/2021	04/2021	41(0) 0	3/4
775	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934]MoRTH,ANDHRA PRADESH ,	03/2018	228.32 -	228.32	105.72	08/2018 -	03/2021	-	2/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
776	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU - [N24000936]MoRTH,ANDHRA PRADESH ,	03/2018	244.95 245.00	244.95	136.22	08/2018 -	-	-	2/3
777	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]MoRTH,ANDHRA PRADESH ,	03/2018	289.67 290.00	289.67	177.78	08/2018 -	02/2021	-	3/4
778	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938]MoRTH,ANDHRA PRADESH ,	03/2018	297.12 294.00	294.12	373.98	07/2018 -	-	-	4/4
779	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]MoRTH,ANDHRA PRADESH ,	03/2018	504.19 504.00	504.19	427.08	11/2018 -	01/2021	-	3/4
780	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]MoRTH,ANDHRA PRADESH ,	03/2016	995.09 995.00	995.09	476.77	05/2016 -	04/2021	59(O) -	3/4
781	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963]MoRTH,ANDHRA PRADESH ,	01/2018	418.03 -	418.03	194.62	08/2018 05/2021	05/2021	33(O) 0	3/4
782	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964]MoRTH,ANDHRA PRADESH ,	08/2016	350.61 -	350.61	323.06	01/2017 -	12/2020	-	3/4
783	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]MoRTH,ANDHRA PRADESH ,	01/2016	386.09 -	386.09	199.35	05/2016 -	-	-	3/4
784	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966]MoRTH,ANDHRA PRADESH ,	01/2016	348.95 -	348.95	200.57	08/2016 -	07/2021	59(O) -	2/4
785	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967]MoRTH,ANDHRA PRADESH ,	03/2016	444.84 -	444.84	304.42	09/2016 -	-	-	3/4
786	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]MoRTH,ANDHRA PRADESH ,	11/2016	376.25 -	376.25	264.97	08/2017 -	-	-	3/4
787	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969]MoRTH,ANDHRA PRADESH ,	01/2017	263.45 -	263.45	97.45	09/2017 -	05/2021	44(O) -	0/4
788	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]MoRTH,ANDHRA PRADESH ,	01/2017	576.48 -	576.48	288.92	01/2018 -	-	-	1/4
789	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S - [N24001183]MoRTH,ANDHRA PRADESH ,	07/2014	251.55 -	251.55	7.74	02/2015 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
790	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105 - [N24001298]NHAI,ANDHRA PRADESH , EPC	09/2018	597.67 -	597.67	.00	01/2020 -	-	-	0/0
791	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN - [N24001299]NHAI,ANDHRA PRADESH , EPC	09/2018	617.41 -	617.41	.00	02/2019 -	-	-	0/0
792	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2019	1,226.88 -	1,226.88	.00	02/2021 -	-	-	0/0
793	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - [N24001301]NHAI,ANDHRA PRADESH , PPP BOT (Hybrid Annuity)	11/2019	1,601.10 -	1,601.10	.00	02/2021 -	-	-	0/0
794	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]MoRTH,ARUNACHAL PRADESH , ITEM RATE	12/2011	156.63 276.00	276.00	.00	02/2012 -	-	-	0/0
795	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]MoRTH,ARUNACHAL PRADESH , ITEM RATE	11/2010	305.49 -	305.49	131.08	03/2011 -	-	-	0/0
796	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]MoRTH,ARUNACHAL PRADESH , ITEM RATE	03/2012	207.03 -	389.45	308.09	05/2012 06/2018	-	-	0/0
797	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH , EPC	07/2015	197.16 -	197.16	91.25	10/2018 -	-	-	2/4
798	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	394.00 -	394.00	400.56	06/2018 -	-	-	3/3
799	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH ,	04/2016	245.79 -	245.79	178.10	- -	-	-	3/4
800	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH ,	04/2016	198.00 -	198.00	184.62	10/2016 -	-	-	3/4
801	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH ,	11/2015	434.06 -	434.06	172.89	- -	-	-	2/4
802	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH ,	12/2016	138.93 155.00	155.00	79.91	01/2017 -	-	-	2/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
803	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH ,	01/2017	1,253.10 -	1,253.10	204.77	03/2017 -	03/2022	60(O) -	1/4
804	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH ,	03/2017	284.09 284.09	284.09	152.19	04/2017 03/2018	03/2021	-	2/4
805	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH ,	02/2017	195.23 -	252.79	102.51	04/2017 -	-	-	2/4
806	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH ,	02/2017	203.36 -	263.31	117.81	04/2017 -	-	-	2/4
807	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH ,	01/2017	194.66 -	252.05	113.63	04/2017 -	-	-	2/4
808	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH ,	02/2017	180.57 -	180.57	52.65	04/2017 -	02/2021	-	1/4
809	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH ,	02/2017	167.28 -	167.28	22.06	04/2017 -	-	-	1/4
810	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH ,	01/2017	198.22 -	252.05	113.63	04/2017 -	-	-	2/4
811	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH ,	03/2018	392.60 -	392.60	.00	- -	-	-	0/0
812	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH ,	12/2016	200.44 -	200.44	115.89	- -	-	-	0/0
813	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH ,	03/2017	1,718.59 -	1,718.59	265.00	- -	-	-	0/0
814	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH ,	09/2016	568.92 -	568.92	260.57	- -	-	-	0/0
815	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH ,	12/2016	188.78 -	188.78	91.23	- -	-	-	0/0
816	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH ,	02/2017	175.06 -	175.06	82.18	- -	04/2022	- -	2/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
817	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL,ARUNACHAL PRADESH ,	02/2017	176.12 -	176.12	67.95	- -	04/2022	- -	2/4
818	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL,ARUNACHAL PRADESH ,	10/2015	210.50 210.50	210.50	145.07	- 01/2016	01/2019	-	3/4
819	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN - [N24000978]NHIDCL,ARUNACHAL PRADESH ,	03/2015	172.75 -	172.75	134.38	- -	-	-	4/4
820	TWO-LANING OF HAYULIANG– HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI - [N24000979]NHIDCL,ARUNACHAL PRADESH ,	01/2017	256.66 -	256.66	24.14	- -	-	-	1/4
821	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH,ARUNACHAL PRADESH ,	09/2011	1,979.00 -	2,036.90	1,237.25	- 03/2020	-	-	0/0
822	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH,ARUNACHAL PRADESH ,	11/2016	243.89 -	243.89	145.31	- -	09/2020	-	0/0
823	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68. - [N24001244]NHIDCL,ARUNACHAL PRADESH , EPC	08/2020	301.06 -	301.06	.00	04/2022 -	04/2022	0(O) -	0/4
824	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO - [N24001245]NHIDCL,ARUNACHAL PRADESH , EPC	09/2020	353.90 -	353.90	4.21	05/2022 -	05/2022	0(O) -	0/4
825	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1) - [N24001289]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	403.68 -	403.68	40.08	02/2020 -	-	-	0/0
826	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2 - [N24001290]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	342.55 -	342.55	144.45	02/2020 -	-	-	0/0
827	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE - [N24001291]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	421.48 -	421.48	24.12	11/2020 -	-	-	0/0
828	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE - [N24001292]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	543.05 -	543.05	86.24	11/2020 -	-	-	0/0
829	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE - [N24001293]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	486.70 -	486.70	54.10	10/2020 -	-	-	0/0
830	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE - [N24001294]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	560.39 -	560.39	118.45	02/2020 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
831	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE - [N24001295]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	347.78 -	347.78	58.02	09/2020 -	-	-	0/0
832	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG - [N24001296]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	394.27 -	394.27	25.72	10/2020 -	-	-	0/0
833	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE - [N24001297]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	450.65 -	450.65	6.51	11/2020 -	-	-	0/0
834	HARANGAJO TO MAIBANG (AS-23) KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM ,	12/2003	280.00 -	520.00	612.58	02/2009 -	-	-	0/0
835	MAIBANG TO LUMDING (AS-25) KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM ,	12/2003	199.81 -	340.14	325.28	04/2009 -	-	-	0/0
836	MAIBANG TO LUMDING (AS-26) KM.60.500 TO KM.83.400 NH-54 - [240106279]NHAI,ASSAM ,	12/2003	167.64 -	435.78	427.96	11/2008 -	-	-	0/0
837	MAIBANG TO LUMDING (AS-24) KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM ,	12/2003	155.04 -	255.23	251.39	11/2008 -	-	-	0/0
838	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM ,	12/2003	245.00 -	174.34	240.36	03/2008 -	08/2020	-	0/0
839	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM ,	12/2003	225.00 -	225.00	390.72	06/2008 -	09/2019	-	0/0
840	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM ,	12/2003	208.00 -	230.00	370.56	04/2008 -	02/2021	-	0/0
841	DHARAMTUL TO SONAPUR KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM ,	12/2003	160.00 -	167.98	233.27	05/2008 -	06/2019	-	0/0
842	HARANGAJO TO MAIBANG NH-54 - [N24000062]NHAI,ASSAM ,	12/2003	196.00 -	655.17	655.17	07/2009 -	-	-	0/0
843	BRAHMPUTRA BRIDGE NH NO-31 - [N24000063]NHAI,ASSAM ,	12/2003	217.61 -	360.84	489.84	04/2010 -	07/2019	-	0/0
844	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM , EPC	05/2015	454.89 -	454.89	175.00	05/2018 -	12/2020	-	2/4
845	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM , EPC	06/2015	437.39 -	407.30	21.46	06/2018 -	12/2021	42(O) -	0/4
846	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM , EPC	06/2015	463.49 -	398.06	59.71	06/2018 -	12/2021	42(O) -	0/4
847	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL,ASSAM , EPC	06/2016	829.00 -	829.00	350.14	01/2019 -	-	-	2/4
848	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM , EPC	03/2015	168.39 -	168.39	134.98	11/2018 -	-	-	4/4
849	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM , EPC	10/2014	588.95 -	588.95	420.91	11/2018 -	-	-	3/4
850	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]MoRTH,ASSAM , EPC	11/2010	268.08 -	390.73	283.52	05/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
851	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]MoRTH,ASSAM , ITEM RATE	11/2010	470.20 -	630.36	386.98	02/2011 -	-	-	0/0
852	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM , EPC	12/2015	223.30 -	223.30	111.16	06/2018 -	-	-	3/4
853	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM , EPC	01/1991	520.01 -	303.49	174.66	- -	-	-	2/4
854	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM , EPC	12/2015	289.99 -	196.24	76.89	12/2018 -	-	-	1/4
855	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM , EPC	01/2016	294.17 -	294.17	121.82	01/2016 -	04/2021	63(O) -	1/4
856	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM , EPC	01/2016	252.00 -	223.50	22.91	01/2016 -	-	-	0/4
857	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM ,	03/2015	829.00 -	829.00	415.82	01/2016 -	-	-	2/3
858	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL,ASSAM ,	10/2017	818.00 -	887.68	151.62	- -	-	-	1/4
859	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0 KM 54/0 TO KM 61/0 KM 69/0 TO KM 80/0 AN - [N24001152]MoRTH,ASSAM ,	09/2018	160.00 -	160.00	101.70	09/2021 -	09/2021	0(O) -	0/0
860	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM - [N24001153]MoRTH,ASSAM ,	11/2010	197.37 -	197.37	88.86	02/2014 -	-	-	0/0
861	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL,ASSAM ,	03/2017	1,049.51 -	273.40	98.01	- -	-	-	0/0
862	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W - [N24001243]MoRTH,ASSAM ,	03/2020	166.94 -	166.94	.00	12/2020 -	-	-	0/0
863	4-LANING OF HAPACHARA - TULUNGIA SECTION - [N24001246]NHIDCL,ASSAM , EPC	03/2020	220.20 -	220.20	.00	12/2022 -	12/2022	0(O) -	0/4
864	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800 - [N24001248]NHIDCL,ASSAM , EPC	08/2020	208.84 -	208.84	.00	04/2022 -	04/2022	0(O) -	0/4
865	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923 - [N24001250]NHIDCL,ASSAM , EPC	08/2020	278.46 -	278.46	12.06	03/2022 -	03/2022	0(O) -	0/4
866	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) - [N24001269]NHIDCL,ASSAM , EPC	03/2020	216.49 -	216.49	3.35	03/2022 -	03/2022	0(O) -	0/4
867	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR , PPP (ANNUITY)	08/2010	671.30 -	671.30	1,360.63	02/2013 -	-	-	3/4
868	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR , PPP (BOT)	09/2011	574.00 -	574.00	768.73	03/2014 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
869	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR ,	10/2011	375.09 -	375.09	494.33	04/2014 -	-	-	0/0
870	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR , PPP (ANNUITY)	01/2011	575.00 -	575.00	555.63	07/2013 -	-	-	2/3
871	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR , PPP (ANNUITY)	05/2011	511.54 585.00	591.00	575.99	11/2013 12/2020	01/2021	-	0/0
872	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH,BIHAR , EPC	01/1991	675.00 -	675.00	294.01	- -	-	-	0/0
873	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MoRTH,BIHAR , ITEM RATE	01/1991	282.41 -	322.01	327.21	08/2016 -	-	-	0/0
874	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MoRTH,BIHAR , ITEM RATE	01/1991	358.22 -	377.64	339.86	10/2016 -	-	-	0/0
875	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR ,	08/2015	556.07 -	556.07	.00	- -	-	-	0/0
876	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR ,	12/2015	1,041.10 -	1,041.10	343.52	04/2019 -	-	-	0/0
877	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR ,	08/2015	814.04 -	825.17	512.04	- -	10/2021	-	2/4
878	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR ,	08/2015	322.09 -	322.09	77.53	04/2018 -	12/2020	-	0/0
879	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR ,	01/1991	642.41 -	681.67	400.60	- -	-	-	1/4
880	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR ,	12/2015	1,167.45 -	1,182.94	186.70	- -	-	-	0/0
881	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR ,	08/2015	399.54 -	297.27	271.39	04/2019 -	-	-	3/4
882	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MoRTH,BIHAR ,	01/1991	478.35 -	478.35	458.03	- -	-	-	0/0
883	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR ,	08/2015	854.80 -	1,038.56	1,160.00	- -	-	-	3/4
884	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR ,	08/2015	516.13 -	649.27	712.15	04/2018 -	-	-	4/4
885	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]MoRTH,BIHAR , EPC	01/1991	154.62 -	154.62	.00	- -	-	-	0/0
886	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]MoRTH,BIHAR , EPC	01/1991	319.68 -	369.77	249.55	- -	-	-	0/0
887	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MoRTH,BIHAR ,	10/2013	278.39 -	278.39	.00	08/2014 -	-	-	0/0
888	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MoRTH,BIHAR ,	11/2013	683.83 -	560.70	671.96	07/2016 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
889	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MoRTH,BIHAR ,	02/2014	665.50 -	665.50	.00	07/2016 -	-	-	0/0
890	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MoRTH,BIHAR ,	02/2016	178.85 -	152.62	116.49	05/2016 -	-	-	0/0
891	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MoRTH,BIHAR ,	02/2016	369.77 -	369.77	.00	06/2016 -	-	-	0/0
892	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MoRTH,BIHAR ,	02/2016	553.30 -	478.35	289.14	05/2016 -	-	-	0/0
893	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH,BIHAR ,	01/2014	1,408.85 -	925.87	745.25	10/2016 -	-	-	0/0
894	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPR - [N24000580]MoRTH,BIHAR ,	03/2015	206.80 -	206.80	74.04	07/2016 -	-	-	0/0
895	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MoRTH,BIHAR ,	08/2015	288.24 -	288.24	303.16	11/2015 -	-	-	0/0
896	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI,BIHAR ,	05/2015	581.84 -	581.84	89.69	05/2017 -	-	-	0/0
897	REHABILITATION OF 4-LANE 5.575 KM LONG 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH,BIHAR ,	08/2016	1,742.01 -	1,742.01	1,233.39	12/2016 -	-	-	0/0
898	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR ,	03/2017	672.89 -	736.01	31.82	03/2020 -	-	-	0/0
899	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR ,	03/2017	235.48 -	227.77	36.08	03/2020 -	05/2021	14(O) -	0/0
900	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR , Central Sector Projects	08/2017	950.64 -	950.64	200.18	08/2017 -	02/2022	54(O) -	0/0
901	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR ,	12/2017	2,598.00 -	2,598.00	.00	- -	-	-	0/0
902	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR ,	01/2018	573.70 -	573.70	44.46	- -	-	-	0/0
903	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR ,	01/2018	895.39 -	895.39	.00	- -	-	-	0/0
904	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR ,	03/2018	496.20 -	537.17	38.11	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
905	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR ,	09/2018	1,478.40 -	1,478.40	1.98	- -	-	-	0/0
906	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C - [N24000999]MoRTH,BIHAR ,	11/2016	230.34 -	230.34	210.12	10/2019 -	-	-	0/0
907	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH,BIHAR ,	03/2018	153.24 -	153.24	72.51	- -	-	-	0/0
908	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]MoRTH,BIHAR ,	05/2014	199.98 -	199.98	174.35	08/2016 -	-	-	0/0
909	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR ,	02/2019	2,926.42 -	2,926.42	2.00	- -	-	-	0/0
910	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT - [N24001303]NHAI,BIHAR , EPC	10/2013	649.90 -	649.90	.00	12/2020 -	-	-	0/0
911	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE - [N24001304]NHAI,BIHAR , EPC	10/2013	446.97 -	446.97	.00	11/2020 -	-	-	0/0
912	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA - [N24001305]NHAI,BIHAR , EPC	10/2013	464.09 -	464.09	.00	11/2020 -	-	-	0/0
913	WIDENING OF SL TO 2 L KM. 107-184.80 SUKUMA TO KONTA ON NH 221 - [N24001223]MoRTH,CHANDIGARH ,	03/2010	179.89 271.00	271.00	270.91	03/2013 05/2019	-	-	0/0
914	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1 - [N24001225]MoRTH,CHANDIGARH ,	12/2010	169.26 299.00	299.00	.00	01/2019 -	-	-	0/0
915	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]MoRTH,CHHATISGARH , EPC	12/2015	291.05 -	291.05	212.46	- 06/2021	06/2021	- 0	0/0
916	REHABILITATION AND UPGRADE OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]MoRTH,CHHATISGARH , EPC	11/2015	485.44 -	485.44	447.13	12/2015 05/2020	05/2020	-	0/0
917	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH ,	12/2015	596.67 -	596.67	426.38	05/2018 -	-	-	0/0
918	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH ,	12/2015	509.13 -	509.13	412.66	04/2018 -	-	-	0/0
919	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH ,	03/2018	1,029.96 -	1,261.05	197.88	- -	03/2021	-	0/0
920	REHABILITATION AND UPGRADE OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]MoRTH,CHHATISGARH ,	01/2016	497.14 572.66	572.66	270.56	08/2016 06/2021	06/2021	58(O) 0	0/0
921	REHABILITATION AND UPGRADE OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218]MoRTH,CHHATISGARH ,	11/2015	335.32 -	335.32	269.15	06/2017 06/2021	06/2021	48(O) 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
922	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]MoRTH,CHHATISGARH ,	01/2016	476.20 543.73	544.00	400.38	09/2016 06/2021	06/2021	57(O) 0	0/0
923	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 127.500 TO 178.944 DARRIGHAT TO BANARI SECTION - [N24001220]MoRTH,CHHATISGARH ,	03/2016	491.52 512.77	491.52	474.52	09/2016 10/2020	10/2020	-	0/0
924	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]MoRTH,CHHATISGARH ,	01/2016	624.98 731.50	731.50	416.16	10/2016 06/2021	06/2021	56(O) 0	0/0
925	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222]MoRTH,CHHATISGARH ,	03/2016	452.94 435.61	435.61	94.34	07/2016 06/2021	06/2021	59(O) 0	0/0
926	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO - [N24001224]MoRTH,CHHATISGARH ,	03/2017	423.79 -	423.79	273.27	01/2018 03/2021	03/2021	-	0/0
927	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226]MoRTH,CHHATISGARH ,	12/2014	496.02 -	496.02	240.11	03/2015 06/2021	06/2021	75(O) 0	0/0
928	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228]MoRTH,CHHATISGARH ,	11/2017	188.80 -	188.80	78.69	05/2019 06/2021	06/2021	25(O) 0	0/0
929	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 - [N24001229]MoRTH,CHHATISGARH ,	12/2014	379.16 -	379.16	272.43	11/2017 06/2021	06/2021	43(O) 0	0/0
930	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8 - [N24001184]NHIDCL,DELHI ,	07/2017	269.69 -	269.69	.00	09/2019 -	-	-	0/0
931	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]MoRTH,GOA , EPC	03/2015	297.00 -	297.00	290.64	04/2018 -	-	-	0/1
932	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]MoRTH,GOA ,	03/2015	298.33 -	298.33	310.72	- -	-	-	0/4
933	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]MoRTH,GOA , EPC	03/2015	184.05 -	184.05	91.39	- -	-	-	2/4
934	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]MoRTH,GOA , EPC	03/2015	280.16 -	290.59	219.47	- -	-	-	3/4
935	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH,GOA , EPC	10/2015	936.40 -	936.40	478.46	- -	-	-	0/0
936	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH,GOA , EPC	12/2015	773.98 -	773.98	336.25	- -	-	-	0/0
937	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MoRTH,GOA , EPC	12/2015	819.95 -	819.95	205.20	- -	-	-	0/0
938	PATRADEVI TO KARASWADA 4L - [N24001004]MoRTH,GOA ,	03/2017	634.32 -	634.32	278.30	05/2020 -	-	-	1/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
939	KARASWADA TO BAMBOLIM - [N24001005]MORTH,GOA ,	03/2017	852.67 -	852.67	138.14	12/2019 -	-	-	1/4
940	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT , PPP (BOT)	03/2010	1,509.10 -	1,509.10	3,684.44	09/2012 -	-	-	2/3
941	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT , PPP (BOT)	01/2011	953.88 -	953.88	976.79	07/2013 -	-	-	0/0
942	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI, GUJARAT , PPP (BOT)	01/2013	2,125.24 -	2,125.24	4,669.71	12/2015 -	-	-	3/3
943	VADODARA-SURAT SECTION - [N24000361]NHAI, GUJARAT ,	03/2014	503.16 -	503.16	389.50	08/2016 -	-	-	0/0
944	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI, GUJARAT ,	05/2016	998.18 -	998.18	719.75	-	-	-	2/2
945	FOUR LANING OF TALAJA - MAHUVA SECTION OF NH - 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI, GUJARAT ,	05/2016	834.64 -	834.64	203.40	-	-	-	1/1
946	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI, GUJARAT ,	05/2016	723.64 -	723.64	503.45	-	-	-	2/2
947	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI, GUJARAT ,	05/2016	763.08 -	763.08	450.54	-	-	-	2/2
948	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI, GUJARAT ,	05/2016	425.60 -	425.60	134.77	-	-	-	0/0
949	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI, GUJARAT ,	05/2016	364.56 -	392.00	353.42	-	04/2021	-	0/0
950	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI, GUJARAT ,	07/2016	829.97 -	829.97	248.88	-	-	-	0/0
951	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI, GUJARAT ,	12/2016	417.19 -	417.19	303.96	-	-	-	0/3
952	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI, GUJARAT ,	01/2017	1,251.11 -	1,251.11	1,084.26	-	-	-	0/0
953	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI, GUJARAT ,	06/2017	1,958.88 -	1,993.81	1,116.85	06/2020 -	02/2021	-	3/3
954	JUNAGADH BYPASS - [N24000701]NHAI, GUJARAT , Central Sector Projects	10/2017	232.49 -	232.49	.00	10/2017 -	-	-	0/0
955	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI, GUJARAT ,	02/2018	1,052.21 -	1,449.00	342.39	-	01/2021	-	0/0
956	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI, GUJARAT ,	03/2018	2,702.05 -	2,043.00	1,327.65	-	06/2021	-	0/0
957	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI, GUJARAT ,	03/2018	1,437.64 -	1,437.64	564.11	-	07/2021	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
958	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT ,	03/2018	1,161.39 -	1,161.39	.00	- -	-	-	0/0
959	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922]MoRTH,GUJARAT , EPC	12/2017	867.97 -	867.97	516.24	11/2018 -	-	-	2/4
960	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEEN - [N24000923]MoRTH,GUJARAT , EPC	03/2018	464.07 -	464.07	302.02	11/2018 -	-	-	3/4
961	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPIR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]MoRTH,GUJARAT , EPC	10/2018	400.76 -	400.76	131.34	05/2019 -	-	-	2/4
962	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926]MoRTH,GUJARAT , EPC	08/2017	962.43 -	962.43	249.39	03/2018 -	-	-	1/4
963	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197]MoRTH,GUJARAT ,	03/2018	351.00 -	351.00	128.70	06/2021 -	06/2021	0(O) -	2/4
964	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA , PPP (BOT)	04/2007	486.00 -	486.00	470.01	05/2010 -	-	-	0/0
965	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA , PPP (BOT)	05/2009	1,108.00 -	2,967.50	3,996.01	11/2011 -	-	-	0/0
966	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA ,	12/2015	602.95 -	507.70	496.22	06/2016 -	-	-	0/0
967	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA ,	01/2016	574.28 -	537.16	516.32	07/2018 -	-	-	0/0
968	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA , PPP (BOT)	07/2015	2,128.72 -	2,128.72	1,070.00	04/2019 -	09/2021	29(O) -	0/0
969	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA ,	08/2016	248.97 -	248.97	270.65	05/2019 -	-	-	0/0
970	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA ,	09/2016	1,004.67 -	813.45	577.21	05/2019 -	-	-	0/0
971	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA ,	03/2017	639.79 -	552.90	597.77	03/2020 05/2021	05/2021	14(O) 0	0/0
972	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA ,	03/2018	1,484.30 -	1,484.30	165.51	- 06/2021	12/2020	-	0/0
973	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA ,	03/2018	275.12 -	275.12	167.13	- -	-	-	0/0
974	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTI - [N24000837]NHAI,HARYANA ,	03/2018	307.79 -	307.79	197.30	- -	-	-	0/0
975	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA ,	03/2018	634.70 -	931.21	268.17	- -	07/2021	- -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
976	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA ,	03/2018	795.50 -	799.30	213.17	- -	07/2021	- -	0/0
977	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA ,	03/2018	198.05 -	198.05	116.46	- -	-	-	0/0
978	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA ,	03/2018	181.78 -	181.78	129.84	- -	-	-	0/0
979	REDESIGNING REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA ,	03/2018	551.58 -	551.58	306.06	- -	-	-	0/0
980	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]MoRTH,HARYANA ,	01/2017	247.25 -	247.25	178.64	03/2019 -	02/2021	-	0/0
981	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) - [N24000908]MoRTH,HARYANA ,	01/2017	276.01 -	276.01	187.39	03/2019 -	-	-	0/0
982	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI,HARYANA ,	01/2019	1,051.91 -	1,051.91	526.09	- -	-	-	0/0
983	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI,HARYANA ,	01/2019	1,120.06 -	1,120.06	501.73	- -	-	-	0/0
984	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA ,	01/2019	1,137.42 -	1,137.42	690.88	- -	-	-	0/0
985	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA ,	01/2019	1,033.19 -	1,033.19	604.45	- -	-	-	0/0
986	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA ,	01/2019	1,243.45 -	1,243.45	659.79	- -	-	-	0/0
987	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA ,	01/2019	889.36 -	889.36	438.38	- -	-	-	0/0
988	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA ,	01/2019	1,018.79 -	1,018.79	468.24	- -	-	-	0/0
989	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA ,	01/2019	996.65 -	996.65	567.52	- -	-	-	0/0
990	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH , PPP (BOT)	11/2013	1,916.79 -	1,916.79	1,960.92	11/2016 -	-	-	0/0
991	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH ,	09/2015	934.46 -	934.46	697.33	03/2018 -	-	-	0/0
992	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH ,	02/2016	273.20 -	273.20	667.10	02/2019 -	-	-	0/0
993	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH ,	08/2016	1,583.18 -	1,583.18	271.06	- -	-	-	0/0
994	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH ,	09/2016	1,273.71 -	1,273.71	663.25	- -	-	-	0/0
995	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH ,	10/2016	447.75 -	447.75	1,160.74	- -	08/2020	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
996	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH ,	06/2017	2,485.93 -	2,485.93	827.64	06/2020 -	09/2021	15(O) -	0/0
997	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050 ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH ,	03/2018	478.74 -	478.74	127.42	- -	05/2021	- -	0/0
998	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,987.00 -	1,987.00	3,108.90	07/2015 -	09/2020	-	0/0
999	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	05/2011	2,159.00 -	2,519.00	4,709.65	06/2015 -	-	-	0/0
1000	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,813.76 -	1,813.76	2,652.11	07/2013 -	-	-	0/0
1001	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	06/2011	1,100.70 -	1,100.70	2,924.02	06/2014 -	10/2020	-	0/0
1002	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR ,	12/2015	2,168.66 -	2,168.66	816.46	06/2019 -	12/2020	-	0/0
1003	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR ,	12/2015	2,136.97 -	2,136.97	1,615.66	12/2018 -	-	-	0/0
1004	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR ,	12/2017	1,471.75 1,339.00	1,339.00	862.50	- -	01/2021	-	2/3
1005	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866]NHIDCL,JAMMU AND KASHMIR ,	03/2018	404.17 -	404.17	163.90	08/2018 -	-	-	2/4
1006	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM - [N24000867]NHIDCL,JAMMU AND KASHMIR ,	03/2018	216.00 -	216.00	82.85	11/2018 -	-	-	1/4
1007	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR ,	03/2018	253.44 -	253.44	51.77	07/2019 -	-	-	0/0
1008	CONSTRUCTION OPERATION AND MAINTENANCE OF Z-MORH TUNNEL INCLUDING APPROACHES ON NH-01 SRINAGAR-SONA - [N24001253]NHIDCL,JAMMU AND KASHMIR ,	12/2019	2,680.42 -	2,680.42	.00	12/2023 -	12/2023	0(O) -	0/4
1009	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D - [N24001256]NHIDCL,JAMMU AND KASHMIR , EPC	08/2020	6,808.69 -	6,808.69	.00	09/2026 -	09/2026	0(O) -	0/6
1010	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL - [N24001264]NHIDCL,JAMMU AND KASHMIR , EPC	07/2020	228.39 -	228.39	.00	04/2022 -	04/2022	0(O) -	0/4
1011	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K - [N24001266]NHIDCL,JAMMU AND KASHMIR , EPC	07/2020	210.79 -	210.79	.00	04/2022 -	04/2022	0(O) -	0/4
1012	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND , PPP (ANNUITY)	12/2012	1,479.00 -	1,479.00	740.26	06/2015 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1013	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND ,	02/2016	997.15 -	1,115.95	975.08	03/2019 -	-	-	0/0
1014	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- [N24000594]NHAI,JHARKHAND ,	07/2016	458.03 -	486.00	432.16	-	-	-	0/0
1015	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND ,	08/2016	323.72 -	336.60	312.79	08/2018 -	-	-	0/0
1016	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND ,	01/2018	273.46 -	276.17	72.53	-	-	-	0/0
1017	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND ,	01/2018	1,155.16 -	1,155.16	366.61	-	-	-	0/0
1018	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND ,	03/2018	1,005.08 -	1,005.08	.00	-	-	-	0/0
1019	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131]MoRTH,JHARKHAND ,	03/2018	212.99 -	212.99	156.72	06/2020 -	01/2021	-	0/0
1020	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I - [N24001216]MoRTH,JHARKHAND ,	12/2016	196.00 -	196.00	47.95	09/2021 -	09/2021	0(O) -	0/4
1021	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA ,	09/2010	946.00 -	946.00	818.53	06/2018 -	-	-	3/3
1022	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA , EPC	03/2015	165.67 -	165.67	.00	11/2015 -	-	-	0/0
1023	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MoRTH,KARNATAKA , EPC	03/2015	159.12 -	159.12	.00	11/2015 -	-	-	0/0
1024	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MoRTH,KARNATAKA , EPC	01/1991	219.40 -	219.40	.00	01/2018 -	-	-	0/0
1025	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA , PPP (BOT)	05/2014	1,655.01 -	1,655.01	1,867.51	08/2016 -	12/2020	-	0/0
1026	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA , PPP (BOT)	03/2015	1,388.00 -	1,388.00	1,295.00	08/2018 -	-	-	0/0
1027	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA ,	03/2016	701.40 -	701.40	132.05	03/2019 03/2022	03/2022	36(O) 0	0/0
1028	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA ,	03/2016	870.00 -	870.00	36.30	03/2019 -	11/2020	-	0/0
1029	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA ,	08/2016	1,664.20 -	1,664.20	1,003.87	04/2020 -	12/2020	-	0/0
1030	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA ,	08/2016	1,167.42 -	870.00	333.68	03/2019 01/2021	12/2021	33(O) 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1031	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA ,	09/2016	950.69 -	1,108.00	1,429.25	08/2019 -	-	-	0/0
1032	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA ,	03/2017	831.58 -	1,177.00	912.40	03/2020 -	-	-	0/0
1033	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA ,	03/2017	993.16 -	1,434.00	1,201.43	03/2020 -	-	-	0/0
1034	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA ,	02/2018	486.78 -	486.78	171.98	- -	-	-	0/0
1035	SIX-LANING OF BANGALORE – NIDAGATTA SECTION KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA ,	02/2018	1,995.34 -	2,400.00	3,088.59	- -	11/2021	- -	0/0
1036	SIX LANING OF NIDAGATTA-MYSORE SECTION KM 74.20 TO KM 135.304 OF NH-275 IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA ,	02/2018	2,177.80 -	2,450.00	2,244.98	- -	-	-	0/0
1037	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT - [N24001154]MoRTH,KARNATAKA ,	08/2016	367.44 -	367.44	61.95	01/2017 -	-	-	0/0
1038	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT - [N24001155]MoRTH,KARNATAKA ,	08/2016	175.20 -	175.20	113.38	01/2017 -	-	-	0/0
1039	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA - [N24001156]MoRTH,KARNATAKA ,	01/2017	166.67 -	166.67	117.05	09/2017 -	-	-	0/0
1040	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA ,	08/2016	175.50 -	175.50	86.54	02/2017 -	-	-	0/0
1041	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA ,	03/2018	159.97 -	159.97	.00	06/2019 -	-	-	0/0
1042	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHA SECTION - [N24001159]MoRTH,KARNATAKA ,	01/2018	159.70 -	159.70	22.79	07/2018 -	-	-	0/0
1043	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA ,	09/2017	191.60 -	191.60	26.24	10/2018 -	-	-	0/0
1044	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- [N24001161]MoRTH,KARNATAKA ,	12/2017	297.30 -	297.30	.00	01/2019 -	-	-	0/0
1045	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA ,	03/2018	325.86 -	325.86	326.88	10/2018 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1046	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]MoRTH,KARNATAKA ,	08/2016	329.01 -	329.01	135.50	02/2017 -	-	-	0/0
1047	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA ,	10/2016	396.96 -	396.96	113.98	03/2017 -	-	-	0/0
1048	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA ,	11/2016	314.90 -	314.90	104.40	03/2017 -	-	-	0/0
1049	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA ,	03/2015	159.12 -	159.12	96.22	01/2016 -	-	-	0/0
1050	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776) - [N24001167]MoRTH,KARNATAKA ,	03/2015	165.67 -	165.67	87.63	01/2016 -	-	-	0/0
1051	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA ,	05/2018	171.60 -	171.60	.86	05/2018 -	-	-	0/0
1052	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM. - [N24001170]MoRTH,KARNATAKA ,	01/2014	471.16 -	471.16	128.32	08/2014 -	-	-	0/0
1053	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA ,	01/2017	291.49 -	291.49	130.00	08/2017 -	-	-	0/0
1054	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA ,	02/2017	157.32 188.00	157.32	.00	05/2019 -	05/2021	24(O) -	0/0
1055	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA , PPP (BOT)	02/2010	617.00 -	617.00	943.17	08/2012 -	-	-	0/0
1056	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]MoRTH,KERALA , EPC	01/2014	255.75 348.00	348.43	290.12	09/2017 -	-	-	0/0
1057	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA ,	06/2015	845.24 -	941.00	889.83	- -	01/2020	-	0/0
1058	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA ,	04/2016	804.97 -	804.97	522.80	06/2018 -	03/2021	-	0/0
1059	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA , Central Sector Projects	09/2017	1,124.11 -	1,232.76	527.67	09/2017 -	05/2021	44(O) -	0/0
1060	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA ,	02/2018	1,424.77 -	1,853.42	14.19	- -	-	-	0/0
1061	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH , PPP (BOT)	10/2010	1,175.00 -	1,175.00	1,509.96	04/2013 -	-	-	4/4
1062	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH , PPP (BOT)	11/2010	325.00 -	475.00	469.54	05/2013 -	-	-	3/3

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1063	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]MoRTH,MADHYA PRADESH , BOT (TOLL)	01/2012	320.48 -	320.48	189.49	08/2015 -	-	-	0/0
1064	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH,MADHYA PRADESH , EPC	06/2015	390.51 -	390.51	257.01	- 03/2021	06/2021	- 0	0/0
1065	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]MoRTH,MADHYA PRADESH , EPC	11/2013	497.05 -	881.05	754.27	05/2017 -	04/2021	47(O) -	0/0
1066	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]MoRTH,MADHYA PRADESH , BOT (TOLL)	08/2015	257.80 -	257.00	12.38	- -	-	-	0/0
1067	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]MoRTH,MADHYA PRADESH , BOT (TOLL)	11/2011	954.43 -	1,191.51	235.61	09/2015 -	10/2021	73(O) -	0/0
1068	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH , BOT (TOLL)	01/2012	410.72 -	410.72	390.00	04/2015 -	03/2021	-	0/0
1069	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH ,	03/2015	795.76 686.13	686.13	669.94	- -	05/2020	-	0/0
1070	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH ,	03/2015	794.30 679.94	691.38	669.35	- -	05/2020	-	0/0
1071	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH , EPC	11/2015	628.45 -	628.45	439.63	01/2020 01/2021	06/2021	17(O) 3	0/0
1072	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]MoRTH,MADHYA PRADESH , EPC	12/2015	957.54 -	957.54	756.69	02/2020 04/2021	04/2021	14(O) 0	0/0
1073	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH ,	03/2015	928.83 -	928.83	824.83	- -	06/2015	-	0/0
1074	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH , PPP (BOT)	05/2013	1,055.00 -	1,601.77	1,393.40	11/2015 -	-	-	0/0
1075	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH ,	06/2015	1,012.90 -	1,012.90	226.10	03/2016 -	-	-	0/0
1076	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH ,	03/2015	810.22 -	810.22	771.23	- 06/2015	06/2015	-	0/0
1077	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADHYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH,MADHYA PRADESH , EPC	03/2015	511.83 -	511.83	375.50	08/2017 06/2021	06/2021	46(O) 0	0/0
1078	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH ,	08/2016	227.49 -	227.49	195.73	01/2019 -	-	-	4/4
1079	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH , Central Sector Projects	10/2017	639.97 -	639.97	473.85	10/2017 -	-	-	3/4
1080	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	374.40 -	204.65	221.79	09/2017 -	-	-	3/4
1081	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	990.61 -	990.61	648.40	09/2017 -	01/2021	-	3/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1082	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH ,	12/2017	950.27 -	950.27	224.81	- -	08/2021	- -	3/4
1083	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH ,	01/2018	960.24 -	960.24	738.74	- -	-	-	0/4
1084	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI,MADHYA PRADESH ,	01/2018	770.73 -	770.73	350.68	- -	07/2018	-	0/0
1085	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH ,	03/2018	162.56 -	162.56	129.98	03/2018 -	06/2021	39(O) -	0/0
1086	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH ,	03/2018	166.21 -	173.41	141.65	08/2018 -	-	-	0/0
1087	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH,MADHYA PRADESH ,	02/2018	169.63 -	169.63	46.52	03/2018 -	06/2021	39(O) -	0/0
1088	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]MoRTH,MADHYA PRADESH ,	11/2017	235.91 -	235.91	176.23	02/2018 02/2021	02/2021	-	0/0
1089	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]MoRTH,MADHYA PRADESH ,	11/2017	184.62 -	184.62	86.32	02/2018 06/2021	06/2021	40(O) 0	0/0
1090	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884]MoRTH,MADHYA PRADESH ,	03/2018	191.21 -	191.21	127.13	11/2019 -	01/2021	-	0/0
1091	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH ,	01/2017	205.05 -	205.05	123.20	03/2017 -	06/2021	51(O) -	0/0
1092	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH ,	03/2018	214.69 -	214.69	69.34	03/2018 -	09/2021	42(O) -	0/0
1093	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]MoRTH,MADHYA PRADESH ,	03/2018	217.22 -	226.88	170.96	08/2018 09/2021	09/2021	37(O) 0	0/0
1094	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH ,	03/2018	233.04 -	233.04	158.22	03/2018 -	06/2021	39(O) -	0/0
1095	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH ,	11/2017	249.05 -	249.05	195.13	07/2018 03/2021	04/2021	33(O) 1	0/0
1096	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]MoRTH,MADHYA PRADESH ,	11/2017	254.17 -	254.17	164.68	02/2018 03/2021	06/2021	40(O) 3	0/0
1097	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH ,	02/2018	279.44 -	279.44	156.14	03/2018 12/2020	06/2021	39(O) 3	0/0
1098	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 - [N24000895]MoRTH,MADHYA PRADESH ,	09/2016	287.34 -	287.34	194.85	01/2019 09/2020	11/2020	-	0/0
1099	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]MoRTH,MADHYA PRADESH ,	01/2017	373.82 -	373.82	197.04	09/2019 06/2021	06/2021	21(O) 0	0/0
1100	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]MoRTH,MADHYA PRADESH ,	01/2016	809.16 -	809.16	573.85	07/2018 05/2021	05/2021	34(O) 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1101	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]MoRTH,MADHYA PRADESH ,	03/2016	877.79 -	877.79	687.99	06/2019 04/2021	04/2021	22(O) 0	0/0
1102	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 - [N24000962]MoRTH,MADHYA PRADESH ,	09/2016	178.23 -	178.23	122.99	09/2018 -	-	-	0/0
1103	ANJANGAON TO MAH/MP BORDER - [N24001007]MoRTH,MADHYA PRADESH ,	01/2017	359.00 359.00	359.00	315.85	06/2019 -	-	-	0/4
1104	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MoRTH,MADHYA PRADESH ,	11/2017	392.33 428.55	428.55	351.92	03/2018 06/2021	06/2021	39(O) 0	0/0
1105	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]MoRTH,MADHYA PRADESH ,	01/2019	264.50 -	264.50	85.70	03/2021 11/2021	11/2021	8(O) 8	0/0
1106	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI,MADHYA PRADESH ,	10/2019	743.88 -	743.89	298.54	- -	12/2021	- -	1/3
1107	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]NHAI,MADHYA PRADESH ,	12/2017	656.98 -	840.00	105.50	- -	11/2022	- -	0/4
1108	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA - [N24001213]NHAI,MADHYA PRADESH ,	12/2017	1,094.97 -	1,094.97	.00	- -	02/2022	- -	2/4
1109	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214]NHAI,MADHYA PRADESH ,	12/2017	217.96 -	884.00	257.13	- -	-	-	1/4
1110	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE - [N24001231]NHAI,MADHYA PRADESH ,	02/2019	990.97 -	990.97	569.29	12/2019 -	12/2021	24(O) -	2/3
1111	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO - [N24001232]NHAI,MADHYA PRADESH ,	02/2019	847.00 -	847.00	393.93	03/2020 -	04/2022	25(O) -	1/3
1112	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS- CONTROLLED EXPRESSWAY FROM BAWDI VILLAG - [N24001233]NHAI,MADHYA PRADESH ,	03/2019	1,047.00 -	1,047.00	367.12	05/2020 -	05/2022	24(O) -	1/3
1113	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T - [N24001234]NHAI,MADHYA PRADESH ,	02/2019	996.27 -	996.27	419.25	03/2020 -	-	-	2/3
1114	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA , PPP (BOT)	10/2010	1,724.55 -	1,724.55	2,559.00	03/2013 -	03/2021	-	0/0
1115	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA , PPP (BOT)	05/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	-	-	2/2

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1116	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]MoRTH,MAHARASHTRA , EPC	03/2015	168.30 -	168.30	80.00	- -	-	-	0/4
1117	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]MoRTH,MAHARASHTRA , EPC	08/2014	187.79 -	187.79	76.62	07/2016 -	-	-	0/12
1118	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]MoRTH,MAHARASHTRA , EPC	01/2014	446.77 -	446.77	300.50	- -	-	-	3/4
1119	WIDENING NH-848 FROM KM 16.000 TO 34.000 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MoRTH,MAHARASHTRA , EPC	10/2015	289.60 -	289.60	90.65	- -	-	-	0/0
1120	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MoRTH,MAHARASHTRA , ITEM RATE	12/2011	156.26 227.00	247.95	175.00	- -	-	-	0/0
1121	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA , EPC	01/2015	225.81 -	225.81	89.93	- -	-	-	0/0
1122	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	2,288.18 -	2,288.18	487.81	05/2019 -	-	-	0/0
1123	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270 (D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA ,	09/2015	414.51 -	414.00	409.16	05/2018 11/2020	11/2020	-	0/1
1124	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA ,	10/2015	531.13 -	730.97	653.06	05/2018 06/2021	06/2021	37(O) 0	0/0
1125	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA , EPC	07/2015	1,885.74 -	1,885.74	1,636.02	05/2019 -	-	-	0/0
1126	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA ,	10/2015	593.26 -	690.17	595.33	05/2018 06/2021	06/2021	37(O) 0	0/1
1127	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB SERVICE ROADS FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA ,	12/2015	649.50 -	649.50	209.18	03/2019 12/2021	03/2022	36(O) 3	0/0
1128	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA ,	08/2015	505.00 -	504.00	385.08	05/2018 04/2019	06/2021	37(O) 0	0/1
1129	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA , PPP (BOT)	01/2015	972.50 -	972.50	1,492.00	07/2017 -	-	-	0/0
1130	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA , PPP (BOT)	06/2014	923.04 -	923.04	861.99	11/2016 -	-	-	0/0
1131	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	1,871.34 -	1,871.34	3,443.43	01/2018 -	-	-	0/0
1132	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA ,	04/2010	1,170.52 -	1,170.52	2,051.36	06/2012 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1133	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA ,	03/2016	197.69 -	197.69	151.11	07/2018 -	-	-	0/0
1134	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA ,	03/2016	546.00 -	546.00	307.08	07/2019 06/2021	12/2021	29(O) 0	0/0
1135	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA ,	03/2016	591.66 -	591.66	318.30	07/2019 06/2021	12/2021	29(O) 0	0/0
1136	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH,MAHARASHTRA ,	03/2016	1,142.62 -	1,142.62	585.85	-	-	-	0/0
1137	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH,MAHARASHTRA ,	03/2016	1,101.58 -	1,101.58	324.00	-	-	-	0/0
1138	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA ,	11/2016	1,071.61 -	1,048.10	965.72	-	07/2021	-	3/4
1139	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA ,	11/2016	1,064.88 -	1,021.00	336.32	-	07/2021	-	1/4
1140	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA ,	11/2016	400.25 -	400.25	105.20	03/2019 -	02/2021	-	0/0
1141	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA ,	11/2016	446.17 -	446.17	70.85	03/2019 -	03/2021	-	0/0
1142	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA ,	11/2016	290.73 -	315.00	246.70	-	-	-	0/0
1143	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA ,	01/2017	244.90 -	244.90	251.87	05/2019 -	-	-	0/0
1144	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA ,	02/2017	904.16 -	904.16	855.25	02/2020 -	-	-	0/0
1145	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA ,	03/2017	247.02 -	157.49	31.97	03/2020 -	-	-	0/0
1146	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA ,	03/2017	744.64 -	982.00	.00	03/2020 -	-	-	0/0
1147	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA ,	03/2017	1,030.44 -	1,065.51	1,015.76	03/2020 -	-	-	0/3
1148	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA ,	03/2017	988.34 -	1,043.28	1,035.00	03/2020 -	-	-	3/3
1149	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA ,	03/2017	1,059.73 -	1,071.00	610.87	03/2017 -	-	-	0/0
1150	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA ,	03/2017	296.19 -	254.00	254.85	03/2020 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1151	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA ,	03/2017	1,098.06 -	1,160.64	1,068.76	03/2020 -	-	-	0/3
1152	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA ,	12/2017	404.94 -	448.18	427.22	- -	10/2020	-	0/0
1153	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA ,	01/2018	607.00 -	607.00	440.92	- -	08/2021	- -	0/1
1154	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA ,	01/2018	621.00 -	621.00	591.21	- -	04/2021	- -	2/3
1155	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA , EPC	03/2018	291.53 -	291.53	150.06	- 08/2021	02/2022	- 0	0/0
1156	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA , EPC	03/2018	289.21 -	289.21	194.57	- 02/2021	08/2021	- 0	0/0
1157	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA ,	03/2018	1,162.92 -	1,162.92	58.20	- -	07/2021	- -	0/0
1158	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA ,	03/2018	642.13 -	807.00	666.56	- -	-	-	0/0
1159	SARSAM TO KOTHARI - [N24001002]MoRTH,MAHARASHTRA ,	02/2016	545.64 -	545.64	166.29	07/2019 -	-	-	0/4
1160	AKOLA TO AKOT - [N24001003]MoRTH,MAHARASHTRA ,	01/2017	313.95 -	313.95	49.38	06/2019 -	-	-	0/4
1161	AKOT TO ANJANGAON - [N24001006]MoRTH,MAHARASHTRA ,	01/2017	245.77 246.00	245.77	197.90	06/2019 -	-	-	0/4
1162	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA ,	02/2017	203.21 203.00	203.21	150.09	05/2019 -	-	-	0/0
1163	SHEGAON TO DEORI PHATA - [N24001010]MoRTH,MAHARASHTRA ,	02/2017	373.10 373.00	373.10	311.65	05/2019 -	-	-	0/4
1164	MEHKAR TO CHIKALI - [N24001011]MoRTH,MAHARASHTRA ,	02/2017	322.48 322.00	322.48	229.08	05/2019 -	-	-	0/4
1165	CHIKALI TO KHAMGAON - [N24001012]MoRTH,MAHARASHTRA ,	02/2017	548.03 548.00	548.03	359.14	06/2019 -	-	-	0/4
1166	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA ,	01/2017	391.06 391.00	391.06	220.42	06/2019 -	-	-	0/0
1167	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA ,	01/2017	385.87 386.00	385.87	258.29	06/2019 -	-	-	0/0
1168	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA ,	01/2017	341.16 341.00	341.16	228.07	06/2019 -	-	-	0/0
1169	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH,MAHARASHTRA ,	01/2017	471.61 472.00	471.61	321.02	06/2019 -	-	-	0/0
1170	DAHEGAON TO KUHI - [N24001017]MoRTH,MAHARASHTRA ,	01/2017	228.89 229.00	228.89	154.69	06/2019 -	-	-	3/4
1171	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA ,	01/2017	392.83 393.00	392.83	273.42	06/2019 -	-	-	0/0
1172	KATOL TO WARUD - [N24001019]MoRTH,MAHARASHTRA ,	01/2017	463.62 664.00	463.62	253.23	06/2019 -	-	-	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1173	AMD TO SAONER - [N24001021]MoRTH,MAHARASHTRA ,	01/2017	396.91 397.00	396.91	280.56	06/2019 -	-	-	3/4
1174	WADI TO ASOLA - [N24001022]MoRTH,MAHARASHTRA ,	01/2017	363.82 364.00	363.82	39.31	09/2019 -	-	-	1/4
1175	NAGAJ TO VAJAPUR - [N24001023]MoRTH,MAHARASHTRA ,	01/2017	376.72 377.00	376.72	224.81	06/2019 -	-	-	0/4
1176	MANGAON TO DIGHI PORT - [N24001024]MoRTH,MAHARASHTRA ,	01/2017	457.52 -	457.52	352.94	07/2019 -	-	-	2/4
1177	INDAPUR TO AGARDANDA - [N24001025]MoRTH,MAHARASHTRA ,	01/2017	355.17 -	355.17	269.58	07/2019 -	-	-	3/4
1178	WAKAN PALI KHOPOLI - [N24001026]MoRTH,MAHARASHTRA ,	01/2017	376.19 -	376.19	55.87	05/2019 -	-	-	1/4
1179	SHAHPUR PATGAON SECTION I - [N24001027]MoRTH,MAHARASHTRA ,	01/2018	150.79 -	150.79	58.79	12/2019 -	-	-	1/4
1180	PATGAON KHOPOLI SECTION I - [N24001028]MoRTH,MAHARASHTRA ,	01/2018	170.00 -	170.00	104.11	12/2019 -	-	-	0/4
1181	AHMADPUR TO PIMPLA - [N24001029]MoRTH,MAHARASHTRA ,	01/2017	422.38 -	422.38	218.78	08/2019 -	-	-	2/4
1182	PIMPLA TO MANJARUMBHA - [N24001030]MoRTH,MAHARASHTRA ,	01/2017	595.77 -	595.77	264.93	08/2019 -	-	-	2/4
1183	MANJUSUMBA TO CHUMBALI - [N24001031]MoRTH,MAHARASHTRA ,	01/2017	228.54 -	228.54	162.30	08/2019 -	-	-	2/4
1184	DEORI TO AMGAON - [N24001032]MoRTH,MAHARASHTRA ,	01/2017	409.62 410.00	409.62	227.76	05/2019 -	-	-	0/4
1185	MANTHA TALUKAS BORDER TO PARTUR - [N24001033]MoRTH,MAHARASHTRA ,	01/2017	486.19 -	486.19	293.39	07/2019 -	-	-	2/4
1186	PARTUR TO MAJALGAON - [N24001034]MoRTH,MAHARASHTRA ,	01/2017	420.57 -	420.57	254.22	07/2019 -	-	-	2/4
1187	MANSAR TO SALAIKHURD - [N24001035]MoRTH,MAHARASHTRA ,	01/2018	418.36 -	418.36	263.13	12/2019 -	-	-	0/4
1188	MAJALGAON TO KAIJ - [N24001036]MoRTH,MAHARASHTRA ,	01/2017	413.99 -	413.99	299.72	07/2019 -	-	-	0/0
1189	KAIJ TO KUSALAM - [N24001037]MoRTH,MAHARASHTRA ,	01/2017	554.78 -	554.78	252.45	07/2019 -	-	-	2/4
1190	MAHAD TO RAIGAD FORT - [N24001038]MoRTH,MAHARASHTRA ,	07/2018	237.40 -	237.40	9.66	05/2020 -	-	-	0/4
1191	JINTUR TO PARBHANI - [N24001039]MoRTH,MAHARASHTRA ,	01/2017	356.66 -	356.66	106.68	- -	-	-	0/4
1192	JAHIRABAD TO LATUR - [N24001040]MoRTH,MAHARASHTRA ,	01/2017	461.96 -	461.96	250.79	11/2019 -	-	-	2/4
1193	SHIROD SHAHPURER TO NANDED - [N24001041]MoRTH,MAHARASHTRA ,	01/2017	211.34 -	211.34	127.67	07/2019 -	-	-	2/4
1194	SALAIKHURD TO TIRORA - [N24001042]MoRTH,MAHARASHTRA ,	01/2018	415.25 415.25	415.25	220.90	12/2019 -	-	-	0/4
1195	NILAJPHATA TO BHANDARA - [N24001043]MoRTH,MAHARASHTRA ,	01/2018	420.63 421.00	420.63	136.88	05/2020 -	-	-	0/4
1196	KALMAB TO RALEGAON - [N24001044]MoRTH,MAHARASHTRA ,	01/2017	467.78 -	467.78	317.91	06/2019 -	-	-	0/4
1197	JALGAON TO BHADGAON - [N24001045]MoRTH,MAHARASHTRA ,	01/2018	307.54 308.00	307.54	198.65	11/2019 -	-	-	0/4
1198	RALEGAON TO RAMTIRTH - [N24001046]MoRTH,MAHARASHTRA ,	01/2017	210.81 -	210.81	128.94	07/2019 -	-	-	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1199	BHADGAON TO CHALISGAON - [N24001047]MoRTH,MAHARASHTRA ,	01/2018	259.55 260.00	259.55	202.34	11/2019 -	-	-	0/0
1200	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA ,	01/2017	232.77 -	232.77	148.53	07/2019 -	-	-	0/0
1201	KARAD TO VITA - [N24001049]MoRTH,MAHARASHTRA ,	01/2018	344.85 245.00	344.85	190.22	12/2019 -	-	-	0/4
1202	VITA TO NAGAJ - [N24001050]MoRTH,MAHARASHTRA ,	03/2018	304.58 305.00	304.58	97.71	12/2019 -	-	-	0/4
1203	NALDURG TO AKKALKOT - [N24001051]MoRTH,MAHARASHTRA ,	02/2018	274.50 275.00	274.50	143.39	12/2019 -	-	-	0/4
1204	SANGOLA TO JATH - [N24001052]MoRTH,MAHARASHTRA ,	01/2018	257.38 257.00	257.38	96.26	12/2019 -	-	-	0/4
1205	KARAD TO TAGAON - [N24001053]MoRTH,MAHARASHTRA ,	01/2017	537.81 538.00	537.81	159.65	06/2019 -	-	-	0/4
1206	TASGAON TO SHIRDHON - [N24001054]MoRTH,MAHARASHTRA ,	01/2017	195.64 196.00	195.64	116.30	11/2019 -	-	-	0/4
1207	HELWAK TO KARAD - [N24001055]MoRTH,MAHARASHTRA ,	02/2017	416.99 -	416.99	208.63	07/2019 -	-	-	0/4
1208	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA ,	02/2017	422.02 422.00	422.02	278.82	07/2019 -	-	-	0/0
1209	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MoRTH,MAHARASHTRA ,	02/2017	407.19 407.00	407.19	108.68	06/2019 -	-	-	0/4
1210	KARWANDI TO RAJURI - [N24001058]MoRTH,MAHARASHTRA ,	03/2018	276.95 277.00	276.95	253.47	12/2019 -	-	-	0/4
1211	SHIVUR TO YEOLA - [N24001059]MoRTH,MAHARASHTRA ,	03/2018	181.08 -	181.08	97.86	12/2019 -	-	-	0/4
1212	PALPHATA TO PHULAMBARI - [N24001060]MoRTH,MAHARASHTRA ,	03/2018	227.19 227.00	227.19	125.23	12/2019 -	-	-	0/4
1213	CHIKALI TO DHAD - [N24001061]MoRTH,MAHARASHTRA ,	03/2018	189.46 189.00	189.46	97.66	12/2019 -	-	-	0/4
1214	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]MoRTH,MAHARASHTRA ,	03/2018	336.21 336.00	336.21	166.82	12/2019 -	-	-	0/4
1215	WADIGODRI TO DHANGRIPIPRI - [N24001063]MoRTH,MAHARASHTRA ,	03/2018	194.23 194.00	194.23	106.23	02/2020 -	-	-	0/4
1216	DHANGRIPIPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]MoRTH,MAHARASHTRA ,	03/2018	217.14 217.00	217.14	131.55	02/2020 -	-	-	0/4
1217	PARBHANI TO GANGKHED - [N24001065]MoRTH,MAHARASHTRA ,	03/2018	238.19 238.00	238.19	139.93	12/2019 -	-	-	0/4
1218	LATUR TO PANGAON - [N24001066]MoRTH,MAHARASHTRA ,	03/2018	336.47 336.00	336.47	394.00	12/2019 -	-	-	0/4
1219	OMREGA TO AUSA - [N24001067]MoRTH,MAHARASHTRA ,	03/2018	272.04 272.00	272.04	218.03	12/2019 -	-	-	0/4
1220	WASHIM TO DASTAPUR - [N24001068]MoRTH,MAHARASHTRA ,	03/2018	165.51 -	165.51	127.54	12/2019 -	-	-	1/4
1221	NANDED TO JALKOT - [N24001069]MoRTH,MAHARASHTRA ,	12/2017	456.93 457.00	456.93	456.93	09/2019 -	-	-	1/4
1222	DASTAPUR TO KARANJA - [N24001070]MoRTH,MAHARASHTRA ,	03/2018	182.63 -	182.63	132.40	12/2019 -	-	-	2/4
1223	JALKOT TO TOGRI - [N24001071]MoRTH,MAHARASHTRA ,	07/2018	299.92 300.00	299.92	51.25	08/2020 -	-	-	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1224	KHERDA TO NAGZARI - [N24001072]MoRTH,MAHARASHTRA ,	03/2018	181.30 -	181.30	138.50	12/2019 -	-	-	0/4
1225	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA ,	09/2018	301.38 301.00	301.38	134.51	08/2020 -	-	-	0/0
1226	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA ,	03/2018	249.29 -	249.29	155.48	12/2019 -	-	-	0/0
1227	OSMANNAGAR TO KUNDRAL - [N24001075]MoRTH,MAHARASHTRA ,	09/2017	344.25 344.00	344.25	128.89	08/2020 -	-	-	0/4
1228	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA ,	03/2018	219.91 -	219.91	123.76	12/2019 -	-	-	0/0
1229	KUNDRAL TO WAZAR - [N24001077]MoRTH,MAHARASHTRA ,	01/2018	225.25 225.00	225.25	199.34	12/2019 -	-	-	2/4
1230	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA ,	03/2018	228.31 -	228.31	54.77	12/2019 -	-	-	0/0
1231	ARDHAPUR TO HIMAYATNAGAR - [N24001079]MoRTH,MAHARASHTRA ,	12/2017	426.06 426.00	426.06	163.86	06/2020 -	-	-	1/4
1232	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA ,	03/2018	256.15 -	256.15	262.63	12/2019 -	-	-	0/0
1233	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]MoRTH,MAHARASHTRA ,	03/2018	294.87 295.00	294.87	96.59	12/2019 -	-	-	1/4
1234	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA ,	03/2018	223.46 -	223.46	21.42	12/2019 -	-	-	0/0
1235	CHIKLI TO TAKARKHED - [N24001083]MoRTH,MAHARASHTRA ,	03/2018	393.10 393.00	393.10	224.68	12/2019 -	-	-	2/4
1236	PAHUR TO BODHWAD - [N24001084]MoRTH,MAHARASHTRA ,	01/2017	244.93 -	244.93	127.80	05/2020 -	-	-	0/4
1237	TAKARKHED TO JALNA - [N24001085]MoRTH,MAHARASHTRA ,	09/2017	417.90 418.00	417.90	199.01	06/2019 -	-	-	0/4
1238	BODHWAD TO STATE BORDER - [N24001086]MoRTH,MAHARASHTRA ,	01/2017	178.26 -	178.26	124.95	07/2019 -	-	-	0/4
1239	MANGRUPHIR TO MAHAN - [N24001087]MoRTH,MAHARASHTRA ,	03/2018	222.13 222.00	222.13	153.84	11/2019 -	-	-	0/4
1240	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA ,	03/2018	177.84 177.00	177.84	110.20	12/2019 -	-	-	0/0
1241	MALEGAON TO RISOD - [N24001089]MoRTH,MAHARASHTRA ,	02/2018	303.24 303.00	303.24	193.15	12/2019 -	-	-	0/4
1242	KOLDE TO KHETIYA - [N24001090]MoRTH,MAHARASHTRA ,	01/2017	509.18 -	509.18	228.82	07/2019 -	-	-	0/4
1243	REHABILITATION AND UPGRADEMENT OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]MoRTH,MAHARASHTRA ,	03/2016	536.65 356.00	536.65	539.35	12/2019 06/2021	06/2021	18(O) 3	0/0
1244	SATARA TO MHASWAD - [N24001092]MoRTH,MAHARASHTRA ,	01/2017	653.46 -	653.46	252.00	07/2019 -	-	-	0/4
1245	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA ,	12/2017	309.94 310.00	309.94	173.78	12/2019 -	-	-	0/0
1246	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA ,	12/2017	244.04 244.00	244.04	142.76	03/2019 -	-	-	0/0
1247	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA ,	01/2017	388.44 -	388.44	187.77	-	-	-	0/0
1248	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA ,	01/2018	264.41 264.00	264.41	165.67	03/2019 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1249	SELDOH TO PANVAR - [N24001097]MoRTH,MAHARASHTRA ,	07/2018	404.33 404.00	404.33	22.40	05/2020 -	-	-	0/4
1250	WARDHA TO HINGAGHAT - [N24001098]MoRTH,MAHARASHTRA ,	01/2018	216.90 217.00	216.90	136.45	12/2019 -	-	-	1/4
1251	MHASWAD TO TEMBHURNI - [N24001099]MoRTH,MAHARASHTRA ,	01/2017	488.60 -	488.60	223.28	07/2019 -	-	-	0/4
1252	AHMEDNAGAR TO BARAMATI - [N24001100]MoRTH,MAHARASHTRA ,	01/2017	955.40 -	955.40	446.67	08/2019 -	-	-	0/4
1253	KURUDWADI TO PANDHARPUR - [N24001101]MoRTH,MAHARASHTRA ,	01/2017	307.63 -	307.63	190.69	07/2019 -	-	-	0/4
1254	PANDHARPUR TO SANGOLA - [N24001102]MoRTH,MAHARASHTRA ,	07/2017	218.38 -	218.38	168.75	07/2019 -	-	-	0/4
1255	SARAD VANI PIMPALGAON - [N24001103]MoRTH,MAHARASHTRA ,	01/2017	250.46 -	250.46	137.63	07/2019 -	-	-	0/4
1256	MALEWADA TO CHIMUR - [N24001104]MoRTH,MAHARASHTRA ,	10/2016	322.55 -	322.55	189.60	06/2019 -	-	-	2/4
1257	CHIMUR TO WARORA - [N24001105]MoRTH,MAHARASHTRA ,	11/2016	467.70 -	467.70	164.90	03/2019 -	-	-	0/4
1258	PEN TO KHOPOLI - [N24001106]MoRTH,MAHARASHTRA ,	03/2018	301.39 302.00	301.39	50.71	03/2018 -	-	-	0/4
1259	PANCHARAL TO MANDANGHAR - [N24001107]MoRTH,MAHARASHTRA ,	07/2018	381.08 302.00	381.08	9.66	05/2020 -	-	-	0/4
1260	CHALISGAON TO NANDGAON - [N24001108]MoRTH,MAHARASHTRA ,	03/2018	206.97 207.00	206.97	135.41	12/2019 -	-	-	0/4
1261	KUSUMBA TO MALEGAON - [N24001109]MoRTH,MAHARASHTRA ,	03/2018	243.45 244.00	243.45	146.88	12/2019 -	-	-	0/4
1262	BAMNI TO NAVEGAON - [N24001110]MoRTH,MAHARASHTRA ,	09/2017	241.69 242.00	241.69	149.29	04/2020 -	-	-	1/4
1263	KOLHA TO NASRATPUR - [N24001111]MoRTH,MAHARASHTRA ,	04/2016	281.78 282.00	281.78	281.73	04/2019 -	-	-	0/4
1264	NASRATPUR TO BARASGAON - [N24001112]MoRTH,MAHARASHTRA ,	07/2016	406.54 407.00	406.54	163.35	09/2019 -	-	-	2/4
1265	BARASGAON TO RAHATEE - [N24001113]MoRTH,MAHARASHTRA ,	07/2016	289.11 290.00	289.11	101.90	09/2018 -	04/2021	31(O) -	0/4
1266	INDAPUR TO VADPALE - [N24001114]MoRTH,MAHARASHTRA ,	01/2017	1,202.52 1,203.00	1,202.52	973.05	12/2019 -	-	-	1/4
1267	VADPALE TO BHOGAN KHURD - [N24001115]MoRTH,MAHARASHTRA ,	01/2017	1,598.47 1,560.00	1,598.47	1,020.24	11/2019 -	-	-	1/4
1268	GADCHIROLI TO MUL - [N24001116]MoRTH,MAHARASHTRA ,	12/2016	484.15 -	484.15	309.38	06/2019 -	-	-	2/4
1269	MUL TO CHANDRAPUR - [N24001117]MoRTH,MAHARASHTRA ,	12/2016	162.34 -	162.34	53.94	07/2019 -	-	-	1/4
1270	SAKOLI TO BHANDARA - [N24001118]MoRTH,MAHARASHTRA ,	01/2017	362.96 -	362.96	87.90	06/2019 -	-	-	0/4
1271	NAGBHID TO ARMORI - [N24001119]MoRTH,MAHARASHTRA ,	09/2016	269.05 -	269.05	222.60	07/2019 -	-	-	0/4
1272	AKKALKOT TO DHUDHNI - [N24001120]MoRTH,MAHARASHTRA ,	04/2016	211.42 -	211.42	131.85	02/2019 -	-	-	0/4
1273	NASHIK TO PETH - [N24001121]MoRTH,MAHARASHTRA ,	12/2015	289.60 -	289.60	210.10	11/2018 -	-	-	0/4
1274	PAITHAN TO SHIRUR - [N24001122]MoRTH,MAHARASHTRA ,	03/2017	341.80 -	341.80	122.32	06/2019 -	-	-	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1275	SHIRUR TO KHARDA - [N24001123]MoRTH,MAHARASHTRA ,	02/2017	381.77 -	381.77	177.79	06/2019 -	-	-	0/4
1276	AURANGABAD TO SILLOD - [N24001124]MoRTH,MAHARASHTRA ,	02/2017	456.32 -	456.32	289.08	06/2019 -	-	-	0/4
1277	SILLOD TO FARDAPUR - [N24001125]MoRTH,MAHARASHTRA ,	02/2017	337.46 -	337.46	94.22	06/2019 -	-	-	0/4
1278	FARDAPUR TO JALGAON - [N24001126]MoRTH,MAHARASHTRA ,	02/2017	456.45 -	456.45	165.74	06/2019 -	-	-	0/4
1279	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA ,	02/2017	406.51 -	406.51	290.69	06/2019 -	-	-	0/0
1280	BHOKAR TO SANSAM - [N24001128]MoRTH,MAHARASHTRA ,	02/2017	295.09 -	295.99	169.64	07/2019 -	-	-	0/4
1281	BHOGAN KHURD TO KASHEDI - [N24001132]MoRTH,MAHARASHTRA ,	09/2017	743.21 743.00	743.21	193.08	06/2021 -	06/2021	0(O) -	1/4
1282	PARSHURAM GHAT TO ARAWALI - [N24001133]MoRTH,MAHARASHTRA ,	04/2016	983.14 983.00	983.14	709.06	12/2019 -	-	-	1/4
1283	KANTE TO WAKED - [N24001134]MoRTH,MAHARASHTRA ,	03/2016	1,230.02 1,230.00	1,230.02	627.51	11/2019 -	-	-	1/4
1284	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA ,	02/2016	1,244.75 1,245.00	1,244.75	837.21	02/2019 -	-	-	0/0
1285	TALGAON TO KALMATH - [N24001136]MoRTH,MAHARASHTRA ,	10/2016	904.70 905.00	904.70	969.90	03/2020 -	-	-	2/4
1286	KALMATH TO ZARAP - [N24001137]MoRTH,MAHARASHTRA ,	09/2016	1,338.13 1,338.00	1,338.13	1,346.39	03/2020 -	-	-	3/5
1287	PARLI PIMPLA DAHIGUDA - [N24001138]MoRTH,MAHARASHTRA ,	02/2017	205.72 206.00	205.72	41.48	06/2019 -	-	-	1/4
1288	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA ,	02/2018	355.99 -	355.99	238.22	12/2019 -	-	-	0/0
1289	WARDHA TO ARVI - [N24001150]MoRTH,MAHARASHTRA ,	02/2018	313.58 -	313.58	127.86	04/2020 -	-	-	0/4
1290	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL,MANIPUR ,	08/2017	517.57 -	457.77	137.04	10/2018 -	10/2021	36(O) -	3/4
1291	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. - [N24001174]MoRTH,MANIPUR ,	10/2016	235.31 -	235.31	184.33	11/2020 -	11/2020	-	0/0
1292	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137 - [N24001268]NHIDCL,MANIPUR , EPC	03/2019	471.00 -	471.00	.00	07/2022 -	07/2022	0(O) -	0/4
1293	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) - [N24001270]NHIDCL,MANIPUR , EPC	03/2020	292.24 -	292.24	1.74	06/2022 -	06/2022	0(O) -	0/4
1294	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) - [N24001271]NHIDCL,MANIPUR , EPC	06/2020	365.53 -	365.53	3.35	08/2022 -	08/2022	0(O) -	0/4
1295	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) - [N24001272]NHIDCL,MANIPUR , EPC	03/2020	167.95 -	167.95	1.12	06/2022 -	06/2022	0(O) -	0/4
1296	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) - [N24001273]NHIDCL,MANIPUR , EPC	07/2020	177.76 -	177.76	.64	08/2022 -	08/2022	0(O) -	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1297	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI - [N24001274]NHIDCL,MANIPUR , EPC	08/2020	379.39 -	379.39	.00	04/2022 -	04/2022	0(O) -	0/4
1298	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO - [N24001275]NHIDCL,MANIPUR , EPC	08/2020	268.98 -	268.98	.00	04/2022 -	04/2022	0(O) -	0/4
1299	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI - [N24001276]NHIDCL,MANIPUR , EPC	08/2020	228.97 -	228.97	.00	04/2022 -	04/2022	0(O) -	0/4
1300	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA ,	12/2015	479.20 -	479.20	712.89	05/2018 -	-	-	0/0
1301	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA ,	04/2017	553.51 -	553.51	75.51	- -	09/2021	- -	2/4
1302	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA ,	03/2019	306.28 -	306.28	78.34	05/2019 -	-	-	1/4
1303	WIDENING TO 2 LANE RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]MoRTH,MIZORAM , ITEM RATE	11/2010	624.41 -	992.67	890.74	03/2011 -	12/2020	-	0/0
1304	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]MoRTH,MIZORAM , ITEM RATE	08/2010	193.69 -	327.92	301.46	10/2010 -	06/2021	128(O) -	0/0
1305	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]MoRTH,MIZORAM , ITEM RATE	08/2010	195.04 -	377.99	331.49	10/2010 -	06/2021	128(O) -	0/0
1306	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM ,	04/2017	519.09 -	519.09	56.58	09/2019 -	04/2023	43(O) -	0/0
1307	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM ,	04/2017	640.07 -	640.07	3.25	09/2019 -	07/2023	46(O) -	0/0
1308	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM ,	04/2017	642.96 -	642.96	82.00	09/2019 -	06/2023	45(O) -	0/0
1309	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM ,	04/2017	473.18 -	473.18	81.00	09/2019 -	04/2023	43(O) -	0/0
1310	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM ,	04/2017	537.82 -	537.82	100.74	09/2019 -	04/2023	43(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1311	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM ,	04/2017	518.53 -	518.53	108.99	09/2019 -	06/2023	45(O) -	0/0
1312	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM ,	04/2017	404.29 -	404.29	17.77	09/2019 -	04/2024	55(O) -	0/0
1313	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM ,	04/2017	428.11 -	428.11	48.03	09/2019 -	09/2023	48(O) -	0/0
1314	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]MoRTH,MIZORAM ,	08/2010	186.96 -	322.24	298.52	09/2014 -	06/2021	81(O) -	0/0
1315	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54 - [N24001277]NHIDCL,MIZORAM , EPC	09/2020	275.02 -	275.02	14.15	10/2022 -	10/2022	0(O) -	0/4
1316	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) - [N24001278]NHIDCL,MIZORAM , EPC	03/2020	206.88 -	206.88	9.33	07/2022 -	07/2022	0(O) -	0/4
1317	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II) - [N24001279]NHIDCL,MIZORAM , EPC	03/2020	216.49 -	216.49	28.93	07/2022 -	07/2022	0(O) -	0/4
1318	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) - [N24001281]NHIDCL,MIZORAM , EPC	03/2020	292.24 -	292.24	29.00	07/2022 -	07/2022	0(O) -	0/4
1319	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV) - [N24001283]NHIDCL,MIZORAM , EPC	03/2020	281.78 -	281.78	38.40	07/2022 -	07/2022	0(O) -	0/4
1320	GWALIOR-JHANSI NH-75 - [N24000089]NHAI,MULTI STATE , PPP (ANNUITY)	12/2003	604.00 -	364.59	334.71	12/2009 -	-	-	0/0
1321	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE , PPP (BOT)	02/2009	1,693.75 -	1,693.75	2,848.49	08/2011 -	-	-	2/2
1322	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE , PPP (ANNUITY)	02/2011	2,498.76 -	2,498.76	2,531.46	08/2014 -	-	-	0/0
1323	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE , PPP (BOT)	09/2011	2,848.00 -	3,379.45	2,901.20	03/2014 -	12/2022	105(O) -	0/0
1324	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE , PPP (BOT)	09/2011	754.00 -	754.00	1,364.18	03/2013 -	-	-	0/0
1325	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE , PPP (BOT)	10/2012	1,928.22 -	3,182.34	3,087.00	04/2015 01/2021	06/2021	74(O) 3	3/4
1326	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE ,	09/2016	1,244.10 -	1,244.10	1,590.00	- -	05/2021	- -	0/0
1327	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE ,	03/2018	1,294.47 -	1,296.00	.00	- -	-	-	0/0
1328	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE ,	03/2018	998.70 -	962.00	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1329	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD MON-TAMLU-MERANGKONG ROAD PHEK- PFUTSERO ROA - [N24000315]MoRTH,NAGALAND , ITEM RATE	12/2010	1,296.00 -	1,296.00	.00	02/2011 -	-	-	0/0
1330	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND ,	03/2016	373.07 -	387.00	245.80	08/2016 -	05/2021	57(O) -	2/4
1331	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND ,	03/2016	396.52 -	339.55	252.49	08/2016 -	05/2021	57(O) -	2/4
1332	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND ,	03/2016	429.52 -	340.00	193.99	08/2016 -	05/2021	57(O) -	2/4
1333	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND ,	02/2017	507.68 -	507.68	129.13	04/2017 -	-	-	1/4
1334	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND ,	02/2017	387.00 -	387.00	283.11	09/2018 -	09/2020	-	2/4
1335	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND ,	03/2018	500.09 336.49	336.49	79.51	09/2018 -	11/2022	50(O) -	0/0
1336	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND ,	03/2018	339.57 -	339.57	141.46	09/2018 -	07/2022	46(O) -	0/0
1337	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND ,	03/2018	239.30 -	239.30	102.01	09/2018 -	05/2022	44(O) -	0/4
1338	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND ,	03/2018	285.68 -	285.68	77.91	09/2018 -	09/2022	48(O) -	0/4
1339	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND ,	03/2018	315.03 -	315.03	88.52	09/2018 -	12/2021	39(O) -	0/4
1340	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND ,	03/2018	240.64 -	240.64	102.51	09/2018 -	12/2021	39(O) -	0/4
1341	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND ,	03/2018	237.72 -	237.72	109.96	09/2018 -	-	-	1/2
1342	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND ,	03/2018	251.97 -	251.97	138.60	09/2018 -	-	-	0/2
1343	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND ,	03/2018	282.98 -	192.60	127.31	09/2018 -	-	-	0/2

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1344	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND ,	03/2018	215.12 -	215.12	100.90	09/2018 -	11/2021	38(O) -	1/4
1345	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND ,	03/2018	215.79 -	215.79	67.30	09/2018 -	12/2021	39(O) -	1/4
1346	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND ,	03/2018	272.89 -	272.89	51.17	09/2018 -	10/2022	49(O) -	0/4
1347	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND ,	03/2018	323.98 -	323.98	42.54	09/2018 -	11/2022	50(O) -	0/4
1348	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]MoRTH,NAGALAND ,	10/2016	167.62 -	167.62	104.39	12/2020 09/2021	12/2020	-	0/0
1349	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]MoRTH,NAGALAND ,	10/2016	172.63 -	172.63	129.65	12/2020 09/2021	12/2020	-	0/0
1350	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND ,	11/2016	336.25 369.96	336.25	322.13	09/2019 11/2020	-	-	0/0
1351	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]MoRTH,NAGALAND ,	03/2017	217.35 -	217.35	97.62	11/2020 05/2021	11/2020	-	0/0
1352	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180]MoRTH,NAGALAND ,	03/2019	237.51 -	237.51	60.04	12/2022 -	12/2022	0(O) -	0/0
1353	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D - [N24001255]NHIDCL,NAGALAND , EPC	09/2020	277.44 -	277.44	.00	10/2022 -	10/2022	0(O) -	0/4
1354	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG - [N24001257]NHIDCL,NAGALAND , EPC	08/2020	159.85 -	159.85	.00	10/2022 -	10/2022	0(O) -	0/4
1355	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES - [N24001258]NHIDCL,NAGALAND , EPC	08/2020	202.36 -	202.36	.00	04/2022 -	04/2022	0(O) -	0/4
1356	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM - [N24001259]NHIDCL,NAGALAND , EPC	09/2020	315.63 -	315.63	.00	04/2022 -	04/2022	0(O) -	0/4
1357	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T - [N24001260]NHIDCL,NAGALAND , EPC	09/2020	257.15 -	257.15	17.77	04/2022 -	04/2022	0(O) -	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1358	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I) - [N24001280]NHIDCL,NAGALAND , EPC	03/2020	320.97 -	320.97	18.73	06/2022 -	06/2022	0(O) -	0/4
1359	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) - [N24001282]NHIDCL,NAGALAND , EPC	03/2020	355.79 -	355.79	31.76	06/2022 -	06/2022	0(O) -	0/4
1360	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III) - [N24001284]NHIDCL,NAGALAND , EPC	03/2020	361.53 -	361.53	13.17	06/2022 -	06/2022	0(O) -	0/4
1361	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV) - [N24001285]NHIDCL,NAGALAND , EPC	03/2020	330.78 -	330.78	23.74	12/2021 -	12/2021	0(O) -	0/4
1362	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) - [N24001286]NHIDCL,NAGALAND , EPC	03/2020	278.95 -	278.95	56.76	06/2022 -	06/2022	0(O) -	0/4
1363	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) - [N24001287]NHIDCL,NAGALAND , EPC	04/2020	330.80 -	330.80	11.57	12/2021 -	12/2021	0(O) -	0/4
1364	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D - [N24001288]NHIDCL,NAGALAND , EPC	08/2020	232.29 -	232.29	.00	04/2022 -	04/2022	0(O) -	0/4
1365	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA , PPP (BOT)	03/2012	1,410.00 -	1,410.00	1,935.14	09/2014 -	-	-	0/0
1366	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA , PPP (BOT)	12/2011	1,047.00 -	1,047.00	1,874.43	06/2014 -	03/2021	-	0/0
1367	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MoRTH,ODISHA , EPC	01/1991	218.63 -	218.63	29.27	10/2017 -	-	-	0/0
1368	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MoRTH,ODISHA ,	01/1991	229.41 -	229.41	6.65	05/2018 -	-	-	0/0
1369	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]MoRTH,ODISHA , EPC	07/2014	342.05 -	342.05	258.91	01/2017 -	-	-	0/0
1370	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA ,	07/2015	1,282.94 -	1,282.94	468.69	- -	03/2021	-	0/0
1371	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA ,	12/2015	752.28 -	752.28	213.52	- -	03/2022	-	0/1
1372	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]MoRTH,ODISHA , EPC	12/2011	159.39 -	159.39	210.29	11/2017 -	-	-	0/0
1373	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH,ODISHA , EPC	12/2011	191.08 -	191.08	99.98	08/2015 -	-	-	0/0
1374	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA ,	02/2016	1,069.65 -	1,069.65	611.71	- -	01/2021	-	0/0
1375	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA ,	09/2016	2,510.04 -	2,510.04	555.68	08/2019 -	03/2021	-	0/0
1376	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA ,	10/2016	1,008.96 -	1,008.96	930.39	- -	06/2021	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1377	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH,ODISHA ,	03/2014	191.50 192.00	192.00	136.19	05/2016 -	-	-	0/0
1378	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MoRTH,ODISHA ,	01/2015	326.63 327.00	326.63	249.26	04/2018 -	-	-	0/0
1379	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MoRTH,ODISHA ,	02/2015	239.91 240.00	160.00	147.25	10/2017 -	-	-	0/0
1380	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MoRTH,ODISHA ,	07/2014	342.05 342.00	342.00	258.91	01/2017 -	-	-	0/0
1381	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH,ODISHA ,	08/2013	171.96 172.00	172.00	88.30	06/2016 -	-	-	0/0
1382	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MoRTH,ODISHA ,	06/2016	157.30 157.00	157.30	97.29	06/2018 -	-	-	0/0
1383	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA ,	03/2017	1,288.07 -	1,420.00	842.24	03/2020 -	06/2021	15(O) -	0/0
1384	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA , Central Sector Projects	07/2017	476.56 -	476.56	52.19	07/2017 -	06/2021	47(O) -	0/0
1385	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA ,	12/2017	686.65 -	686.65	227.63	- -	06/2021	- -	0/0
1386	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA ,	12/2017	417.51 -	417.51	127.61	- -	06/2021	- -	0/0
1387	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA ,	01/2018	953.09 -	953.09	332.04	- -	03/2022	- -	0/0
1388	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA ,	01/2018	668.86 -	668.86	276.59	- -	06/2021	- -	0/0
1389	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA ,	01/2018	633.68 -	633.68	63.98	- -	-	-	0/1
1390	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA ,	01/2018	614.48 -	614.48	217.40	- -	08/2021	-	0/0
1391	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA ,	01/2018	564.66 -	564.66	240.00	- -	08/2021	-	0/1
1392	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA ,	01/2018	686.65 -	686.65	261.74	- -	06/2021	-	0/0
1393	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK - [N24000737]NHAI,ODISHA ,	01/2018	1,522.00 -	1,522.00	304.40	- -	06/2021	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1394	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA ,	01/2018	999.00 -	999.00	102.70	- -	06/2021	- -	0/0
1395	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA ,	01/2018	503.88 -	503.88	25.40	- -	06/2021	- -	0/0
1396	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA , EPC	03/2018	806.11 -	806.11	189.70	- -	04/2021	- -	0/0
1397	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26. - [N24000911]MoRTH,ODISHA ,	03/2016	165.06 -	165.06	92.59	12/2016 -	-	-	0/0
1398	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MoRTH,ODISHA ,	08/2016	287.70 -	287.70	153.90	02/2017 -	-	-	0/0
1399	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH,ODISHA ,	09/2016	295.67 -	295.67	127.75	02/2017 -	-	-	0/0
1400	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH,ODISHA ,	12/2016	223.50 -	223.50	44.52	08/2018 -	-	-	0/0
1401	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH,ODISHA ,	12/2016	206.88 -	206.88	41.69	04/2018 -	-	-	0/0
1402	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH,ODISHA ,	03/2018	214.23 -	214.23	23.44	08/2018 -	-	-	0/0
1403	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH,ODISHA ,	03/2018	199.16 -	199.16	25.63	08/2018 -	-	-	0/0
1404	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]MoRTH,PUNJAB , EPC	12/2015	766.36 -	766.36	685.36	- -	-	-	0/0
1405	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]MoRTH,PUNJAB , EPC	11/2015	847.02 -	847.02	795.30	- -	-	-	0/0
1406	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]MoRTH,PUNJAB , EPC	11/2015	889.24 -	904.82	754.06	- -	12/2020	-	0/0
1407	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB ,	09/2014	479.00 -	479.00	456.80	- -	07/2021	- -	0/0
1408	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB ,	10/2015	447.29 -	746.43	676.33	12/2017 -	-	-	0/0
1409	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]MoRTH,PUNJAB , EPC	06/2015	892.17 -	892.17	648.44	- -	-	-	0/0
1410	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB ,	08/2016	1,388.34 -	2,587.50	1,569.38	09/2019 -	-	-	0/0
1411	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB ,	08/2016	1,169.61 -	2,280.00	1,282.04	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1412	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB ,	03/2017	754.54 -	756.27	379.05	03/2020 -	12/2021	21(O) -	0/0
1413	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB ,	02/2018	261.76 -	207.00	200.74	- -	07/2021	- -	0/0
1414	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB , EPC	03/2018	199.90 -	199.90	124.52	- -	-	-	0/0
1415	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB , EPC	03/2018	196.05 -	196.05	143.03	- -	-	-	0/0
1416	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905]MoRTH,PUNJAB ,	03/2018	322.48 -	322.48	271.72	07/2020 -	08/2021	13(O) -	0/0
1417	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906]MoRTH,PUNJAB ,	03/2018	173.24 -	173.24	114.55	06/2020 -	-	-	0/0
1418	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]MoRTH,PUNJAB ,	03/2018	293.10 -	293.10	156.80	08/2020 -	-	-	0/0
1419	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH,PUNJAB ,	10/2017	1,069.59 -	1,069.59	692.14	10/2019 -	08/2021	22(O) -	0/0
1420	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH,PUNJAB ,	03/2018	170.57 -	170.57	54.53	11/2020 -	05/2021	6(O) -	0/0
1421	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927]MoRTH,PUNJAB ,	03/2018	293.64 -	293.64	28.24	08/2020 -	-	-	0/0
1422	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]MoRTH,PUNJAB ,	03/2018	293.64 -	293.64	246.29	08/2020 -	-	-	0/0
1423	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MoRTH,RAJASTHAN , EPC	10/2014	269.22 -	269.22	33.24	01/2015 -	-	-	0/0
1424	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MoRTH,RAJASTHAN , EPC	10/2014	257.09 -	257.09	14.18	01/2015 -	-	-	0/0
1425	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MoRTH,RAJASTHAN , EPC	10/2013	278.87 -	278.87	.00	05/2014 -	-	-	0/0
1426	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MoRTH,RAJASTHAN , ITEM RATE	01/1991	376.52 -	376.52	.00	04/2014 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1427	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MoRTH, RAJASTHAN , EPC	02/2015	383.40 -	383.40	244.68	03/2015 -	-	-	0/0
1428	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MoRTH, RAJASTHAN , EPC	12/2015	621.43 -	621.43	387.22	06/2018 -	-	-	0/4
1429	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI, RAJASTHAN ,	09/2014	425.19 -	425.19	276.40	09/2016 -	-	-	0/0
1430	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI, RAJASTHAN ,	10/2015	597.00 -	597.00	587.64	10/2017 -	-	-	3/4
1431	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI, RAJASTHAN , PPP (BOT)	11/2012	530.07 -	530.07	556.02	08/2016 -	06/2020	-	0/0
1432	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI, RAJASTHAN , PPP (BOT)	08/2014	822.90 -	822.90	1,688.16	04/2018 -	-	-	0/0
1433	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]MoRTH, RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	2,323.04	10/2013 -	-	-	0/0
1434	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]MoRTH, RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	492.00	10/2013 -	-	-	0/4
1435	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI, RAJASTHAN , PPP (BOT)	02/2008	1,673.70 -	1,673.70	3,326.93	10/2011 -	-	-	0/0
1436	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS - DHOLPUR - [N24000520]NHAI, RAJASTHAN ,	08/2015	275.90 -	275.90	289.13	-	-	-	0/0
1437	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI, RAJASTHAN , PPP (BOT)	06/2016	637.18 -	637.18	550.35	06/2019 -	09/2019	-	0/0
1438	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI, RAJASTHAN , PPP (BOT)	06/2016	763.23 -	763.23	191.80	06/2019 -	-	-	1/1
1439	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI, RAJASTHAN ,	06/2016	649.00 -	649.00	620.03	06/2019 -	-	-	0/0
1440	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI, RAJASTHAN ,	07/2016	688.70 -	688.70	870.48	-	-	-	0/0
1441	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI, RAJASTHAN ,	07/2016	331.46 -	331.46	267.94	10/2018 -	-	-	0/0
1442	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI, RAJASTHAN ,	09/2016	1,239.82 -	1,727.66	1,674.80	-	01/2021	-	3/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1443	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN ,	09/2016	1,100.19 -	1,145.31	1,327.00	- -	03/2021	-	0/0
1444	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN ,	12/2016	1,031.95 -	1,031.95	374.05	- -	09/2021	-	0/0
1445	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN ,	04/2017	894.00 -	929.32	810.00	04/2020 -	07/2021	15(O) -	0/0
1446	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN , Central Sector Projects	10/2017	964.17 -	964.17	773.03	10/2017 -	11/2020	-	0/0
1447	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJI WAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN ,	12/2017	1,308.73 -	1,308.73	330.46	- -	-	-	0/0
1448	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN ,	02/2018	1,103.88 -	1,103.88	673.70	- -	09/2020	-	0/0
1449	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN ,	02/2018	741.86 -	741.86	168.78	- -	-	-	0/0
1450	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN ,	02/2018	716.76 -	716.76	610.56	- -	-	-	0/0
1451	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN ,	03/2018	874.25 -	874.25	886.59	- -	-	-	0/0
1452	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN ,	03/2018	1,158.35 -	1,158.35	611.28	- -	-	-	0/0
1453	WIDENING STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950]MoRTH,RAJASTHAN ,	11/2017	187.82 -	187.82	131.74	04/2018 -	03/2021	-	2/4
1454	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709 - [N24000957]MoRTH,RAJASTHAN ,	11/2017	163.95 -	163.95	116.47	04/2018 -	03/2021	-	3/4
1455	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000958]MoRTH,RAJASTHAN ,	02/2018	370.30 -	370.30	290.00	06/2018 -	04/2021	34(O) -	1/4
1456	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000959]MoRTH,RAJASTHAN ,	02/2018	341.79 -	341.79	208.00	05/2018 -	06/2021	37(O) -	1/4
1457	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MoRTH,RAJASTHAN ,	03/2019	178.13 -	178.13	139.26	- -	03/2021	-	0/0
1458	NAGAU-BIKANER SECTION FROM KM 177.00 TO KM 267.325 ON NH-89 - [N24001240]MoRTH,RAJASTHAN ,	03/2020	370.36 -	370.36	90.45	08/2022 -	08/2022	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1459	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGOUR SECTION BY EXECUTING BALANCE WORK FRO - [N24001241]MoRTH,RAJASTHAN ,	03/2020	255.23 -	255.23	1.66	08/2020 -	08/2022	24(O) -	0/0
1460	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K - [N24001242]MoRTH,RAJASTHAN ,	08/2020	196.23 -	196.00	.00	11/2020 -	08/2022	21(O) -	0/0
1461	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]MoRTH,SIKKIM ,	04/2013	151.59 370.01	370.01	281.74	08/2013 06/2021	06/2021	94(O) 0	0/0
1462	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]MoRTH,SIKKIM , ITEM RATE	04/2013	166.27 359.92	359.92	243.59	08/2013 06/2021	06/2021	94(O) 0	0/0
1463	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]MoRTH,SIKKIM , ITEM RATE	01/2013	182.28 369.64	369.64	274.07	02/2013 06/2021	06/2021	100(O) 0	0/0
1464	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM , Central Sector Projects	04/2017	388.00 -	447.37	261.20	10/2017 -	-	-	3/4
1465	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA - [N24000766]NHIDCL,SIKKIM ,	04/2017	318.42 -	318.42	66.63	11/2017 -	-	-	2/4
1466	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM ,	03/2017	375.80 -	375.80	52.88	- -	-	-	1/4
1467	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM ,	11/2017	290.05 -	290.05	97.21	11/2017 -	-	-	1/4
1468	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM ,	03/2018	264.84 -	264.84	.00	06/2018 -	-	-	0/4
1469	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N - [N24001251]NHIDCL,SIKKIM , EPC	03/2019	402.94 -	402.94	.00	04/2022 -	04/2022	0(O) -	0/4
1470	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 - [N24001252]NHIDCL,SIKKIM , EPC	08/2020	295.97 -	295.97	.00	04/2023 -	04/2023	0(O) -	0/4
1471	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 - [N24001254]NHIDCL,SIKKIM , EPC	03/2020	242.97 -	242.97	.00	06/2022 -	06/2022	0(O) -	0/4
1472	CONSTRUCTION & UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24001261]NHIDCL,SIKKIM , EPC	08/2020	311.00 -	311.00	.00	04/2023 -	04/2023	0(O) -	0/4
1473	CONSTRUCTION & UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24001262]NHIDCL,SIKKIM , EPC	07/2020	345.38 -	345.38	.00	04/2023 -	04/2023	0(O) -	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1474	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU , PPP (BOT)	09/2011	1,250.00 -	1,250.00	1,337.11	12/2013 -	-	-	0/0
1475	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU ,	06/2011	600.00 -	600.00	1.65	06/2013 -	10/2020	-	0/0
1476	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU , PPP (ANNUITY)	05/2010	374.00 -	166.90	54.22	05/2013 -	08/2021	99(O) -	0/0
1477	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU , PPP (ANNUITY)	04/2012	624.00 -	624.00	8.56	04/2014 -	01/2022	93(O) -	0/0
1478	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MoRTH,TAMIL NADU , EPC	03/2015	258.97 -	268.92	223.10	08/2015 -	-	-	0/0
1479	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MoRTH,TAMIL NADU , EPC	03/2015	157.18 162.00	162.00	146.79	07/2015 -	-	-	0/0
1480	CONSTRUCTION OF PAVED SHOULDERS INCLUDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MoRTH,TAMIL NADU , EPC	11/2015	154.14 -	154.14	140.64	08/2015 -	-	-	0/0
1481	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU ,	05/2015	1,387.11 -	1,387.11	980.46	11/2017 -	-	-	0/0
1482	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU ,	06/2015	563.92 -	563.92	93.53	12/2017 -	-	-	0/0
1483	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU ,	07/2014	401.11 -	401.11	273.89	01/2017 -	-	-	0/0
1484	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU , PPP (BOT)	03/2007	516.00 -	516.00	886.96	07/2008 -	-	-	0/0
1485	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU ,	02/2016	707.82 -	707.82	421.01	08/2018 -	03/2021	-	0/0
1486	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU ,	02/2016	641.17 -	641.17	395.10	07/2018 -	02/2021	-	0/0
1487	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DSIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU ,	03/2017	848.45 932.23	848.45	222.06	03/2020 -	12/2021	21(O) -	0/0
1488	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU , Central Sector Projects	03/2016	641.17 -	641.17	394.32	07/2016 -	02/2021	-	0/0
1489	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU , Central Sector Projects	08/2017	1,176.37 -	1,176.37	462.14	08/2017 -	07/2022	59(O) -	0/0
1490	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU , Central Sector Projects	09/2017	244.27 -	244.27	182.00	09/2017 -	-	-	0/0
1491	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU , Central Sector Projects	09/2017	1,227.87 -	1,227.87	566.14	09/2017 -	07/2022	58(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1492	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU ,	12/2017	379.90 -	379.90	203.77	- -	03/2021	-	0/0
1493	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU ,	02/2018	1,166.26 -	1,296.93	220.78	- -	08/2021	-	0/0
1494	FOUR LANING OF CHETTICKULAM TO NATHAM SECTION OF NH-785 FROM CHETTICKULAM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU , EPC	03/2018	505.35 -	505.35	243.30	- -	08/2021	-	0/0
1495	FOUR LANING OF MADURAI- CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICKULAM (7/300) - [N24000827]NHAI,TAMIL NADU , EPC	03/2018	628.71 -	628.71	310.06	- -	12/2021	-	0/0
1496	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU ,	03/2018	633.55 -	482.04	.00	- -	-	-	0/0
1497	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU ,	03/2018	1,016.92 -	1,071.00	218.47	- -	01/2022	-	0/0
1498	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU ,	03/2018	2,065.96 -	2,169.00	.00	- -	-	-	0/0
1499	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE - [N24001236]CPWD,TAMIL NADU ,	03/2019	297.55 -	297.55	45.52	11/2019 -	-	-	0/0
1500	WIDENING TO 4 LANE / 4 LANE WITH PAVED SHOULDERS WITH STRENGTHENING OF EXISTING CARRIAGEWAY IN KM 0/- [N24001237]MoRTH,TAMIL NADU ,	01/2016	162.72 -	162.72	136.46	09/2016 -	-	-	0/0
1501	CONSTRUCTION OF FLYOVER FROM KM 604/252 TO 607/060 (MARTHANDAM JUNCTION) AND FROM KM 630/116 TO 631/- [N24001238]MoRTH,TAMIL NADU ,	05/2016	307.70 -	307.70	312.82	01/2017 -	-	-	0/0
1502	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM - [N24001239]MoRTH,TAMIL NADU ,	03/2018	240.38 -	240.38	74.56	06/2019 -	-	-	0/0
1503	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA - [N24001302]NHAI,TAMIL NADU , EPC	07/2020	3,426.00 -	3,426.00	.00	12/2021 -	12/2021	0(O) -	0/0
1504	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA , PPP (BOT)	04/2014	1,266.60 -	1,544.00	1,446.45	09/2016 -	-	-	0/0
1505	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]MoRTH,TELANGANA , EPC	01/2014	270.00 -	270.00	19.84	03/2016 -	-	-	1/4
1506	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA , EPC	03/2015	153.21 -	153.21	100.95	01/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1507	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA ,	12/2015	1,423.96 -	1,056.08	974.60	11/2018 07/2019	03/2021	-	0/0
1508	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA ,	03/2017	4,429.00 -	4,429.00	.00	03/2017 -	-	-	0/0
1509	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K - [N24000804]NHAI,TELANGANA ,	03/2018	802.65 -	802.65	380.83	- -	-	-	0/0
1510	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA ,	03/2018	950.63 -	950.63	557.08	- -	-	-	0/0
1511	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA ,	03/2018	857.62 -	857.62	217.06	- -	-	-	0/0
1512	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI,TELANGANA ,	03/2018	828.29 -	828.29	.00	- -	-	-	0/0
1513	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA ,	10/2016	298.32 -	298.32	115.53	02/2019 -	-	-	0/0
1514	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA ,	10/2016	248.83 -	248.83	116.36	03/2019 -	-	-	0/0
1515	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037 OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH,TELANGANA ,	01/2017	244.54 -	244.54	164.33	05/2019 -	-	-	0/0
1516	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON- THIRUMALAGIRI OF NH - [N24000983]MoRTH,TELANGANA ,	01/2017	196.52 -	196.52	107.70	10/2019 -	-	-	0/0
1517	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]MoRTH,TELANGANA ,	01/2017	283.00 -	283.00	228.79	12/2019 -	-	-	0/0
1518	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]MoRTH,TELANGANA ,	01/2017	359.27 -	359.27	293.94	05/2019 -	-	-	0/0
1519	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH,TELANGANA ,	01/2017	300.00 -	300.00	184.77	05/2019 -	-	-	0/0
1520	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]MoRTH,TELANGANA ,	01/2018	283.15 -	283.15	105.53	05/2020 -	-	-	0/0
1521	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]MoRTH,TELANGANA ,	01/2018	230.03 -	230.03	207.56	12/2019 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1522	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]MoRTH, TELANGANA ,	02/2018	206.13 -	206.13	171.37	06/2020 -	-	-	0/0
1523	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH, TELANGANA ,	02/2018	294.13 -	294.13	116.69	11/2019 -	-	-	0/0
1524	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH, TELANGANA ,	02/2018	220.28 -	220.28	124.56	11/2019 -	-	-	0/0
1525	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]MoRTH, TELANGANA ,	02/2018	426.52 -	426.52	388.63	04/2020 -	-	-	0/0
1526	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]MoRTH, TELANGANA ,	03/2018	322.81 -	322.81	142.01	09/2020 -	-	-	0/0
1527	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]MoRTH, TELANGANA ,	03/2018	626.76 -	626.76	177.70	07/2020 -	-	-	0/0
1528	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH, TELANGANA ,	01/2017	605.08 -	605.08	398.78	10/2019 -	-	-	0/0
1529	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH, TELANGANA ,	03/2018	192.67 -	192.67	144.28	07/2019 -	-	-	0/0
1530	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH, TELANGANA ,	01/2019	193.19 -	193.19	61.94	-	-	-	0/0
1531	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL, TRIPURA , EPC	10/2014	369.00 -	369.00	322.69	03/2018 -	-	-	3/4
1532	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]MoRTH, TRIPURA ,	10/2016	171.90 -	171.90	123.81	08/2020 -	07/2021	11(O) -	0/0
1533	2-LANING FROM MANU-SIMLUNG (PKG I) - [N24001247]NHIDCL, TRIPURA , EPC	03/2020	247.76 -	247.76	2.60	01/2022 -	01/2022	0(O) -	0/4
1534	2-LANING FROM MANU-SIMLUNG (PKG III) - [N24001249]NHIDCL, TRIPURA , EPC	06/2020	347.36 -	347.36	.00	01/2022 -	01/2022	0(O) -	0/4
1535	REHABILITATION & UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION - [N24001263]NHIDCL, TRIPURA , EPC	06/2020	277.50 -	277.50	.00	01/2022 -	01/2022	0(O) -	0/4
1536	REHABILITATION & UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE SE - [N24001265]NHIDCL, TRIPURA , EPC	03/2020	154.51 -	154.51	.00	07/2022 -	07/2022	0(O) -	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1537	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID - [N24001267]NHIDCL,TRIPURA , EPC	03/2020	178.43 -	178.43	.00	07/2022 -	07/2022	0(O) -	0/4
1538	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307]MoRTH,TRIPURA , EPC	01/2017	197.67 -	197.67	5.75	12/2022 -	12/2022	0(O) -	0/0
1539	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH , PPP (BOT)	02/2011	1,141.00 -	1,141.00	1,715.42	08/2013 -	-	-	0/0
1540	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH , PPP (BOT)	07/2012	291.36 469.31	469.31	459.07	01/2014 12/2020	12/2020	-	0/0
1541	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH , PPP (BOT)	03/2013	1,573.00 -	1,573.00	2,093.25	09/2015 -	-	-	0/0
1542	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MoRTH,UTTAR PRADESH , EPC	01/2014	282.41 -	282.41	155.53	03/2016 -	-	-	0/0
1543	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH ,	05/2015	261.09 -	261.09	240.96	05/2017 -	-	-	0/0
1544	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH ,	04/2014	351.34 417.68	417.68	433.68	01/2016 12/2020	12/2020	-	0/0
1545	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH ,	09/2015	368.73 -	368.73	239.04	09/2016 -	-	-	0/0
1546	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI,UTTAR PRADESH ,	04/2014	495.78 627.93	627.93	633.24	01/2016 01/2020	01/2020	-	0/0
1547	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]MoRTH,UTTAR PRADESH , EPC	10/2013	445.89 -	653.29	464.05	03/2017 -	-	-	0/0
1548	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]MoRTH,UTTAR PRADESH , ITEM RATE	11/2010	305.49 -	305.49	.00	03/2017 -	-	-	0/0
1549	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH , PPP (BOT)	07/2015	1,657.20 -	1,657.20	2,345.00	01/2019 -	-	-	0/0
1550	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH ,	12/2015	611.65 -	611.65	728.24	06/2016 -	-	-	0/0
1551	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH ,	01/2016	815.28 -	815.28	520.89	06/2018 -	-	-	0/0
1552	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH ,	01/2016	1,027.53 -	1,027.53	601.13	06/2018 -	-	-	0/0
1553	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH ,	06/2016	667.00 -	667.00	464.05	07/2018 -	-	-	0/0
1554	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH ,	12/2015	667.00 -	667.00	549.07	06/2018 -	-	-	0/0
1555	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH,UTTAR PRADESH , EPC	05/2013	164.54 -	164.54	128.54	08/2015 -	-	-	0/0
1556	MEERUT-BULANDSHAHAH - [N24000539]NHAI,UTTAR PRADESH ,	01/2016	683.24 -	987.94	867.27	- -	-	-	0/2
1557	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH ,	01/2016	1,081.57 -	1,057.60	596.79	06/2019 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1558	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH ,	03/2016	676.73 -	676.73	977.26	04/2019 -	-	-	0/0
1559	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH ,	03/2016	1,404.50 -	1,404.50	2,977.58	- -	-	-	0/0
1560	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 TO 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH ,	03/2016	1,396.74 -	1,396.74	227.26	- -	-	-	0/0
1561	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 TO 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH ,	03/2016	1,587.49 -	2,982.00	276.87	04/2019 -	-	-	0/0
1562	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH ,	03/2016	899.00 -	899.00	641.51	04/2019 -	-	-	0/0
1563	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH ,	03/2016	1,668.00 -	1,668.00	946.08	- -	-	-	0/0
1564	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH ,	03/2016	1,408.00 -	1,408.00	442.70	- -	-	-	0/0
1565	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH ,	03/2016	1,737.00 -	1,737.00	1,159.07	- -	-	-	0/0
1566	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH ,	08/2016	2,016.00 -	2,016.00	1,996.00	04/2019 -	-	-	0/0
1567	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH ,	12/2016	534.55 -	531.00	433.62	- -	-	-	0/0
1568	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH ,	01/2017	450.68 -	450.68	397.62	- -	-	-	0/0
1569	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH ,	03/2017	1,373.28 -	1,373.28	974.57	03/2020 -	-	-	2/4
1570	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH ,	03/2017	1,184.71 -	1,310.00	1,039.23	03/2020 -	-	-	3/4
1571	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH ,	03/2017	1,989.00 -	1,989.00	756.92	03/2020 -	-	-	0/0
1572	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH ,	03/2017	2,064.99 -	2,447.00	2,357.84	03/2020 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1573	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH ,	12/2017	1,232.21 -	1,087.00	1,059.17	- -	-	-	0/0
1574	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH ,	12/2017	207.00 -	207.00	43.23	- -	-	-	0/0
1575	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH ,	12/2017	305.00 -	305.00	.00	- -	-	-	0/0
1576	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH ,	01/2018	450.77 -	450.77	.00	- -	-	-	0/0
1577	FOR REHABILITATION AND UPGADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH ,	02/2018	670.50 -	670.50	75.10	- -	-	-	0/0
1578	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH ,	03/2018	809.07 -	809.07	517.66	- -	-	-	0/0
1579	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH ,	03/2018	925.40 -	1,197.00	1,011.70	- -	-	-	0/0
1580	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH ,	03/2018	1,117.84 -	1,117.84	.00	- -	12/2021	-	0/0
1581	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH ,	03/2018	2,140.93 -	2,140.93	1,344.09	- -	-	-	0/0
1582	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH ,	03/2018	1,120.57 -	1,332.00	1,118.92	- -	-	-	0/0
1583	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH ,	03/2018	1,025.80 -	677.07	222.94	- -	-	-	0/0
1584	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH ,	03/2018	1,115.28 -	770.04	332.69	- -	-	-	0/0
1585	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH ,	02/2018	972.77 -	972.77	494.71	- -	-	-	0/0
1586	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH ,	11/2016	326.99 327.00	326.99	105.89	- -	09/2021	-	0/0
1587	REHABILITATION AND UPGADATION OF HARPALPUR -SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942]MoRTH,UTTAR PRADESH ,	03/2016	208.50 -	208.50	165.82	11/2019 -	02/2021	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1588	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA - [N24001139]MoRTH,UTTAR PRADESH ,	10/2016	218.94 219.00	218.94	120.69	03/2020 -	-	-	0/0
1589	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]MoRTH,UTTAR PRADESH ,	11/2016	215.16 215.00	215.16	160.61	09/2019 -	-	-	0/0
1590	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH,UTTAR PRADESH ,	03/2016	240.30 240.00	240.30	210.10	01/2020 -	03/2021	-	0/0
1591	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO - [N24001143]MoRTH,UTTAR PRADESH ,	10/2016	176.94 177.00	176.94	141.11	10/2018 -	-	-	0/0
1592	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]MoRTH,UTTAR PRADESH ,	10/2013	445.89 653.00	653.29	754.40	03/2017 -	04/2021	49(O) -	0/0
1593	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH - [N24001145]MoRTH,UTTAR PRADESH ,	05/2013	164.54 165.00	164.54	141.33	08/2015 -	01/2021	-	0/0
1594	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]MoRTH,UTTAR PRADESH ,	03/2016	249.50 -	249.50	221.17	05/2019 -	03/2021	-	0/0
1595	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2- - [N24001147]MoRTH,UTTAR PRADESH ,	10/2016	239.63 -	239.63	212.53	02/2019 -	-	-	0/0
1596	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148]MoRTH,UTTAR PRADESH ,	03/2016	599.34 -	599.34	492.15	01/2020 -	-	-	0/0
1597	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH – 14 - [N24001185]NHAI,UTTAR PRADESH , PPP BOT (Hybrid Annuity)	11/2017	2,159.00 -	2,159.00	1,363.84	01/2019 -	-	-	0/0
1598	REHABILITATION AND UPGRADATION OF BARAICH -SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA - [N24001202]MoRTH,UTTAR PRADESH ,	03/2016	388.83 -	388.83	304.70	12/2019 -	-	-	0/0
1599	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203]MoRTH,UTTAR PRADESH ,	10/2016	218.90 -	218.90	145.28	03/2020 -	03/2021	-	0/0
1600	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]MoRTH,UTTAR PRADESH ,	07/2016	208.88 -	208.88	175.79	10/2019 -	03/2021	-	0/0
1601	R AND U FROM KM 385.00 TO KM 420.000 TO 2-LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404 - [N24001205]MoRTH,UTTAR PRADESH ,	12/2016	209.10 -	209.10	201.70	10/2019 -	04/2020	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1602	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]MoRTH,UTTAR PRADESH ,	03/2018	263.89 -	242.05	188.43	04/2020 -	04/2021	12(O) -	0/0
1603	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]MoRTH,UTTAR PRADESH ,	03/2018	185.18 -	185.18	124.59	02/2020 -	01/2021	-	0/0
1604	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208]MoRTH,UTTAR PRADESH ,	03/2018	288.30 -	288.30	153.66	08/2020 -	03/2021	-	0/0
1605	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]MoRTH,UTTAR PRADESH ,	03/2016	296.50 -	296.50	199.95	09/2020 -	05/2021	8(O) -	0/0
1606	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH,UTTAR PRADESH ,	03/2018	306.59 -	306.59	.00	- -	-	-	0/0
1607	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH,UTTAR PRADESH ,	11/2018	281.45 -	281.45	.00	- -	-	-	0/0
1608	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 KM - [N24001230]MoRTH,UTTAR PRADESH ,	11/2018	281.45 -	281.45	72.05	12/2020 -	06/2021	6(O) -	0/0
1609	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN - [N24001306]NHAI,UTTAR PRADESH , EPC	10/2020	724.60 -	724.60	.00	03/2023 -	03/2023	0(O) -	0/0
1610	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND ,	11/2011	478.51 -	478.00	315.11	10/2013 -	-	-	0/0
1611	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND ,	03/2016	720.00 -	720.00	348.16	- -	-	-	0/0
1612	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND ,	03/2016	1,443.00 -	1,443.00	1,246.85	- -	-	-	0/0
1613	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND ,	11/2012	605.84 -	722.46	722.46	07/2018 -	-	-	0/0
1614	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND ,	03/2018	274.31 -	274.31	29.13	05/2018 -	-	-	2/4
1615	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND ,	03/2018	403.36 -	403.36	99.65	06/2018 -	-	-	2/4
1616	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND ,	03/2018	417.24 -	417.24	112.62	05/2018 -	-	-	2/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1617	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH,UTTARAKHAND ,	12/2017	257.34 -	257.34	62.79	12/2019 -	-	-	0/0
1618	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH,UTTARAKHAND ,	12/2017	200.34 -	200.34	31.00	12/2019 -	-	-	0/0
1619	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MoRTH,UTTARAKHAND ,	12/2017	248.22 -	248.22	57.20	12/2019 -	-	-	0/0
1620	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MoRTH,UTTARAKHAND ,	06/2017	282.08 -	282.08	77.05	06/2019 -	-	-	0/0
1621	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH,UTTARAKHAND ,	11/2017	232.81 -	232.81	59.44	11/2019 -	-	-	0/0
1622	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH,UTTARAKHAND ,	11/2017	283.51 -	283.51	126.38	11/2019 -	-	-	0/0
1623	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH,UTTARAKHAND ,	11/2017	266.52 -	266.52	144.27	11/2019 -	-	-	0/0
1624	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MoRTH,UTTARAKHAND ,	02/2018	418.88 -	418.88	88.00	02/2020 -	-	-	0/0
1625	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MoRTH,UTTARAKHAND ,	02/2018	293.68 -	293.68	11.57	-	-	-	0/0
1626	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MoRTH,UTTARAKHAND ,	05/2018	248.00 -	248.00	.00	05/2020 -	-	-	0/0
1627	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH,UTTARAKHAND ,	03/2018	460.73 -	461.00	.00	-	-	-	0/0
1628	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL,UTTARAKHAND ,	03/2018	1,383.78 -	1,383.78	148.70	07/2018 -	-	-	1/5
1629	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND ,	08/2016	234.88 -	208.89	118.26	12/2017 -	-	-	0/0
1630	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL , PPP (BOT)	02/2011	1,078.84 -	1,078.84	2,295.18	08/2013 -	05/2021	93(O)	3/4
1631	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL , PPP (BOT)	02/2011	998.79 -	998.79	1,878.70	08/2013 -	06/2022	106(O)	3/4
1632	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL , PPP (BOT)	04/2012	1,396.18 -	1,396.18	2,894.94	09/2014 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1633	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MoRTH, WEST BENGAL ,	01/1991	322.00 -	322.00	56.41	03/2018 -	-	-	0/0
1634	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL ,	10/2015	361.15 -	363.93	272.98	- -	-	-	0/0
1635	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL ,	12/2015	1,083.00 -	1,827.15	2,082.19	06/2018 -	-	-	0/0
1636	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL , PPP (BOT)	04/2014	1,665.00 -	2,360.65	4,472.01	- -	-	-	0/0
1637	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK HALDIA - [N24000553]NHAI, WEST BENGAL ,	03/2016	229.37 -	229.37	130.72	11/2018 -	-	-	0/0
1638	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL ,	09/2016	767.03 -	767.03	604.65	08/2018 -	-	-	0/0
1639	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI, WEST BENGAL ,	03/2018	1,261.98 -	1,952.20	934.06	- -	07/2021	-	0/0
1640	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B NH-31C NH-31 NH-10 O - [N24000871]MoRTH, WEST BENGAL ,	08/2014	600.87 720.97	720.97	682.36	11/2017 -	-	-	0/0
1641	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717 NH-31 NH-31C NH-317A O - [N24000873]MoRTH, WEST BENGAL ,	08/2014	823.20 937.76	937.76	807.99	11/2017 -	-	-	0/0
1642	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]MoRTH, WEST BENGAL ,	01/2017	396.86 396.86	396.86	242.98	09/2019 11/2020	05/2021	20(O) 0	0/0
1643	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879]MoRTH, WEST BENGAL ,	03/2017	202.69 202.69	202.69	144.89	11/2019 -	-	-	0/0
1644	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]MoRTH, WEST BENGAL ,	02/2018	426.18 426.18	426.18	249.01	09/2020 -	12/2021	15(O) -	0/0
1645	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]MoRTH, WEST BENGAL ,	02/2018	218.70 218.70	218.70	104.09	11/2020 04/2020	04/2021	5(O) 0	0/0
1646	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE BAGDO - [N24000883]MoRTH, WEST BENGAL ,	03/2018	254.30 254.30	254.30	103.21	10/2020 -	03/2021	-	0/0
1647	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH, WEST BENGAL ,	03/2016	160.27 213.97	213.97	25.64	08/2019 -	11/2022	39(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1648	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH, WEST BENGAL ,	06/2016	236.78 263.26	263.26	65.84	08/2019 -	12/2021	28(O) -	0/0
1649	REHABILITATION AND UPGRADE OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]MoRTH, WEST BENGAL ,	04/2014	279.70 398.52	398.52	322.91	08/2017 01/2020	02/2020	-	0/0
	Total		5,40,947.36 -	5,61,176.00	3,51,797.31				353/1239
	<u>SHIPPING AND PORTS</u>								
1650	JAL MARG VIKAS PROJECT - [N25000072]IWAI, MULTI STATE ,	01/2018	5,369.18 -	4,633.81	1,871.35	03/2023 -	03/2023	0(O) -	0/0
	Total		5,369.18 -	4,633.81	1,871.35				0/0
	<u>TELECOMMUNICATIONS</u>								
1651	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE (NICF) AT GHIT - [N28000115]CPWD, DELHI ,	10/2016	248.20 -	248.20	145.26	03/2018 -	06/2021	39(O) -	0/0
1652	NETWORK FOR SPECTRUM - [N26000101]DOT, MULTI STATE ,	03/2012	13,334.00 -	24,664.00	17,845.00	07/2015 -	07/2021	72(O) -	0/0
1653	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114]BSNL, MULTI STATE , Central Sector Projects	03/2020	431.16 431.00	431.16	.00	06/2021 -	11/2021	5(O) -	0/0
	Total		14,013.36 -	25,343.36	17,990.26				0/0
	<u>URBAN DEVELOPMENT</u>								
1654	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]PATNA METRO RAIL, BIHAR ,	02/2019	13,365.77 -	13,365.77	231.97	06/2024 -	06/2024	0(O) -	0/0
1655	CONSTRUCTION 729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV-112 TYPE V-68 TYPE VI-5) SHOPS CO - [N28000149]CPWD, CHHATISGARH ,	05/2019	299.97 -	299.97	.29	09/2020 -	-	-	0/0
1656	DELHI MRTS PHASE-III - [N28000056]DMRC, DELHI ,	09/2011	38,585.00 -	38,585.00	39,182.53	03/2016 -	09/2021	66(O) -	0/0
1657	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD, DELHI ,	07/2012	884.30 -	884.30	812.00	12/2015 -	-	-	0/0
1658	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC, DELHI ,	06/2012	4,264.00 -	4,720.73	4,683.08	11/2019 -	-	-	3/7
1659	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG NEW DELHI - [N28000087]CPWD, DELHI ,	06/2015	197.33 -	197.33	106.16	04/2019 06/2021	12/2021	32(O) 2	1/2
1660	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC, DELHI ,	07/2016	2,694.00 -	2,694.00	744.73	- -	12/2022	- -	0/9
1661	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS MINTO ROAD NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD, DELHI ,	11/2017	238.56 -	238.56	157.67	05/2020 -	-	-	1/2

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1662	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI ,	10/2016	422.00 -	422.00	70.75	03/2021 07/2021	07/2021	4(O) 0	0/0
1663	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI ,	10/2016	392.00 -	392.00	73.79	08/2020 -	03/2022	19(O) -	0/0
1664	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI - [N28000123]CPWD,DELHI ,	07/2017	218.72 -	218.72	126.16	11/2020 -	-	-	0/2
1665	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I - [N28000128]CPWD,DELHI ,	10/2016	1,180.00 -	1,100.80	35.63	07/2021 -	12/2024	41(O) -	0/0
1666	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]CPWD,DELHI ,	10/2016	1,128.00 -	1,128.00	22.00	03/2022 -	03/2022	0(O) -	0/0
1667	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS - [N28000135]DMRC,DELHI ,	07/2019	24,948.65 -	24,948.65	1,763.02	03/2025 -	03/2025	0(O) -	0/0
1668	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136]DMRC,DELHI ,	05/2017	565.00 -	565.00	438.37	12/2020 -	09/2021	9(O) -	0/0
1669	C/O STEEL STRUCTURE BUILDINGS USING PRE-ENGINEERED TECHNOLOGY AT AFRICA AVENUE AND KG MARG - [N28000143]CPWD,DELHI ,	02/2020	532.00 -	532.00	150.00	11/2020 -	-	-	0/0
1670	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT ,	11/2014	10,773.00 -	12,787.00	8,768.08	12/2018 -	08/2022	44(O) -	0/0
1671	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137]MEGA,GUJARAT ,	03/2019	5,384.17 -	5,384.17	63.77	03/2024 -	03/2024	0(O) -	0/0
1672	SURAT METRO RAIL PROJECT - [N28000138]MEGA,GUJARAT ,	03/2019	12,020.32 -	12,020.32	20.65	03/2024 -	03/2024	0(O) -	0/0
1673	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA ,	02/2014	26,405.14 30,695.12	30,695.12	17,021.86	02/2019 03/2021	06/2024	64(O) 0	120/249
1674	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA ,	07/2012	5,181.79 -	6,218.14	6,059.17	07/2017 -	09/2020	-	0/0
1675	BHOPAL METRO RAIL - [N28000124]MPMRCL,MADHYA PRADESH ,	11/2018	6,941.40 -	6,941.40	174.53	02/2023 -	02/2023	0(O) -	0/0
1676	INDORE METRO RAIL - [N28000125]MPMRCL,MADHYA PRADESH ,	11/2018	7,500.80 -	7,500.80	130.21	02/2023 -	02/2023	0(O) -	0/0
1677	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA ,	08/2014	8,680.00 -	8,680.00	7,068.52	03/2018 -	-	-	0/0
1678	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA ,	07/2013	23,136.00 -	33,406.00	17,039.36	01/2015 -	03/2023	98(O) -	0/0
1679	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA ,	12/2016	11,420.00 11,420.00	11,420.00	6,214.58	11/2021 -	11/2021	0(O) -	0/0
1680	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134]NCRTC,MULTI STATE ,	03/2019	30,274.00 -	30,274.00	3,416.31	06/2025 -	06/2025	0(O) -	0/0
1681	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU ,	02/2009	14,600.00 -	19,058.00	16,365.87	12/2015 -	-	-	14/24
1682	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU ,	06/2016	3,770.00 -	3,770.00	3,088.12	03/2018 -	03/2021	-	5/21
1683	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH ,	01/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 -	-	-	0/0
1684	KANPUR METRO RAIL PROJECT - [N28000144]LMRCL,UTTAR PRADESH , Public Private (SPV)	05/2019	11,076.48 -	11,076.48	.00	03/2024 -	03/2024	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1685	AGRA METRO RAIL PROJECT - [N28000145]LMRCL,UTTAR PRADESH , Public Private (SPV)	05/2019	8,379.62 -	8,379.62	.00	03/2024 -	03/2024	0(O) -	0/0
1686	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND ,	12/2008	114.26 266.00	266.00	.00	12/2013 -	-	-	0/0
	Total		2,82,500.28 -	3,05,097.88	1,36,565.95				144/316
	<u>WATER RESOURCES</u>								
1687	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA,ANDHRA PRADESH , National Project	02/2009	10,151.04 55,548.87	55,548.87	17,325.20	03/2020 11/2021	04/2022	25(O) 0	0/19
1688	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR ,	10/2005	956.00 -	721.37	712.37	03/2015 -	-	-	5/7
1689	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026]BUIDCO,BIHAR ,	03/2018	230.06 -	230.06	73.63	07/2021 -	07/2021	0(O) -	0/0
1690	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO,BIHAR ,	10/2017	254.13 -	254.13	.05	09/2020 -	-	-	0/0
1691	I AND D AND STP AT CHAPPRA - [N30000028]BUIDCO,BIHAR ,	11/2018	236.15 -	236.15	46.50	12/2020 06/2021	04/2021	4(O) 0	0/0
1692	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]BUIDCO,BIHAR ,	03/2018	305.19 -	305.19	.00	08/2021 -	12/2021	4(O) -	0/0
1693	SEWER NETWORKS SPS AND STP MUNGER - [N30000036]BUIDCO,BIHAR ,	03/2018	294.02 -	294.02	.00	10/2021 -	10/2021	0(O) -	0/0
1694	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]BUIDCO,BIHAR ,	12/2014	225.77 -	225.77	276.57	03/2020 -	03/2021	-	0/0
1695	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR - [N30000038]BUIDCO,BIHAR ,	04/2015	184.93 -	184.93	163.36	04/2020 -	06/2021	14(O) -	0/0
1696	SAIDPUR SEWER NETWORK PATNA - [N30000039]BUIDCO,BIHAR ,	04/2015	268.63 -	268.63	296.97	01/2021 -	-	-	0/0
1697	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]BUIDCO,BIHAR ,	05/2017	356.37 -	356.37	93.34	04/2021 -	04/2021	0(O) -	0/0
1698	SEWERAGE SCHEME AT PAHARI ZONE IVA S PATNA - [N30000041]BUIDCO,BIHAR ,	05/2017	184.86 -	184.86	152.78	05/2021 -	05/2021	0(O) -	0/0
1699	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]BUIDCO,BIHAR ,	05/2017	191.62 -	191.62	54.96	11/2020 03/2021	-	-	0/0
1700	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]BUIDCO,BIHAR ,	03/2017	277.42 -	277.42	146.23	05/2021 -	05/2021	0(O) -	0/0
1701	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]BUIDCO,BIHAR ,	08/2017	578.89 -	578.89	40.09	06/2022 -	06/2022	0(O) -	0/0
1702	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE PATNA - [N30000051]BUIDCO,BIHAR ,	08/2017	824.00 -	824.00	40.09	06/2022 -	06/2022	0(O) -	0/0
1703	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014]DJB,DELHI ,	03/2017	665.78 -	665.78	194.55	12/2022 -	12/2022	0(O) -	0/0
1704	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015]DJB,DELHI ,	05/2016	211.79 -	211.79	87.31	12/2021 -	12/2022	12(O) -	0/0
1705	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]DJB,DELHI ,	05/2016	239.11 -	239.11	129.67	02/2022 -	12/2022	10(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1706	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND MAT CORONATION PILLAR DELHI - [N30000017]DJB,DELHI ,	12/2018	515.07 -	515.07	336.27	01/2021 -	06/2021	5(O) -	0/0
1707	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018]DJB,DELHI ,	05/2017	344.81 -	344.81	.00	05/2020 -	-	-	0/0
1708	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPB,MAHARASHTRA ,	03/2017	233.57 -	233.57	173.71	12/2019 -	12/2021	24(O) -	0/0
1709	INTERCEPTION DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006]UPJalNigam,UTTAR PRADESH ,	05/2017	767.59 -	767.59	76.71	09/2021 -	09/2021	0(O) -	0/0
1710	INTEGRATED PROJECT FOR DEVELOPMENT OF STPS IN ALLAHABAD ALONG WITH EXISTING ASSETS - [N30000007]UPJalNigam,UTTAR PRADESH ,	03/2018	904.00 -	904.00	136.55	09/2021 -	09/2021	0(O) -	0/0
1711	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]UPJalNigam,UTTAR PRADESH ,	10/2017	213.62 261.12	261.12	.00	03/2022 -	03/2022	0(O) -	0/0
1712	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR - [N30000009]UPJalNigam,UTTAR PRADESH ,	10/2016	370.40 430.49	430.49	376.22	08/2020 03/2021	-	-	0/0
1713	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010]UPJalNigam,UTTAR PRADESH ,	03/2018	967.23 -	967.23	40.59	09/2021 -	09/2021	0(O) -	0/0
1714	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA - [N30000011]UPJalNigam,UTTAR PRADESH ,	02/2017	161.31 -	161.31	91.38	11/2019 -	03/2021	-	0/0
1715	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY UTTAR PRADESH - [N30000013]UPJalNigam,UTTAR PRADESH ,	03/2019	271.39 -	271.39	.00	08/2021 -	08/2021	0(O) -	0/0
1716	MATHURA SEWERAGE SCHEME - [N30000019]UPJalNigam,UTTAR PRADESH ,	12/2017	460.45 -	460.45	216.89	12/2020 -	05/2021	5(O) -	0/0
1717	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020]UPJalNigam,UTTAR PRADESH ,	02/2011	279.91 330.05	330.05	244.84	12/2019 -	01/2021	-	0/0
1718	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]UPJalNigam,UTTAR PRADESH ,	01/2019	231.79 -	234.03	.00	12/2021 -	12/2021	0(O) -	0/0
1719	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022]UPJalNigam,UTTAR PRADESH ,	01/2019	206.05 -	206.05	29.26	10/2021 -	10/2021	0(O) -	0/0
1720	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]UPJalNigam,UTTAR PRADESH ,	02/2019	681.78 -	690.71	.00	06/2022 -	06/2022	0(O) -	0/0
1721	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]UPJalNigam,UTTAR PRADESH ,	03/2019	298.12 213.91	213.91	.00	07/2021 -	06/2022	11(O) -	0/0
1722	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI - [N30000003]UKJalNigam,UTTARAKHAND ,	03/2017	273.37 -	273.37	80.45	08/2019 -	-	-	0/0
1723	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH - [N30000004]UKJalNigam,UTTARAKHAND ,	03/2017	158.00 -	158.00	79.00	11/2019 03/2021	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1724	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]KMDA, WEST BENGAL ,	01/2019	384.96 -	384.96	.00	04/2022 -	04/2022	0(O) -	0/0
1725	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPUR - [N30000030]KMDA, WEST BENGAL ,	03/2019	287.53 -	287.53	.00	04/2022 -	04/2022	0(O) -	0/0
1726	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]KMDA, WEST BENGAL ,	12/2018	234.31 -	234.31	.00	04/2022 -	04/2022	0(O) -	0/0
1727	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]KMDA, WEST BENGAL ,	05/2018	198.43 224.69	224.69	.00	02/2022 -	06/2022	4(O) -	0/0
1728	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033]KMDA, WEST BENGAL ,	03/2018	165.16 -	165.16	.00	06/2022 -	06/2022	0(O) -	0/0
1729	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA - [N30000034]KMDA, WEST BENGAL ,	08/2017	307.12 -	307.12	.00	09/2022 -	09/2022	0(O) -	0/0
1730	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH - [N30000042]KMDA, WEST BENGAL ,	05/2018	160.00 154.73	154.73	.00	02/2022 -	10/2022	8(O) -	0/0
1731	INTERCEPTION DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]KMDA, WEST BENGAL ,	08/2017	185.22 -	185.22	.00	12/2021 -	12/2021	0(O) -	0/0
1732	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046]KMDA, WEST BENGAL ,	02/2014	274.76 -	274.76	202.13	12/2019 05/2021	05/2021	17(O) 0	0/0
1733	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]KMDA, WEST BENGAL ,	12/2014	272.32 -	272.32	220.73	04/2020 -	03/2021	-	0/0
1734	INTERCEPTION DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048]KMDA, WEST BENGAL ,	01/2018	172.10 -	172.10	.00	12/2021 -	12/2021	0(O) -	0/0
1735	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]KMDA, WEST BENGAL ,	10/2017	164.93 -	164.93	.00	12/2021 -	12/2021	0(O) -	0/0
	Total		26,781.06 -	72,049.94	22,138.40				5/26
	<u>DEFENCE PRODUCTION</u>								
1736	RESIDENTIAL QUARTERS FOR HAL BANGLORE - [N28000103]CPWD, KARNATAKA ,	12/2016	246.31 -	210.00	131.46	02/2020 -	12/2021	22(O) -	6/10
	Total		246.31 -	210.00	131.46				6/10
	<u>COMMERCE</u>								
1737	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI NEW DELHI - [N40000003]NBCC, DELHI ,	06/2018	302.64 -	302.64	60.00	10/2020 -	-	-	0/0
	Total		302.64 -	302.64	60.00				0/0
	Grand Total		22,33,409.23	26,71,440.77	13,16,032.62				3075/5908

Summary of projects in the Flash Report for the month of April, 2021


Project Implementation - Current Status:

Number of Projects in Previous Month **1737**

Number of Projects in Current Month **1737**

Brief Analysis

Project Status with respect to Original Schedule: Out of 1737 projects, 11 projects are ahead of schedule, 213 projects are on schedule 525 projects are delayed. 882 projects do not have fixed dates of commissioning. 106 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

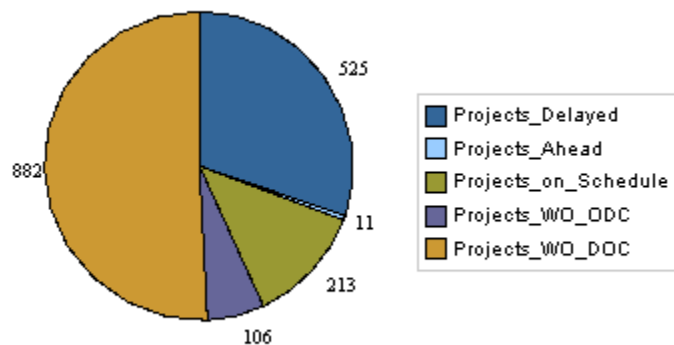


Total No Of Project's:- 1737

Investment Scenario

Total original cost of implementation of 1737 projects when sanctioned, was of the order of Rs. 2233409.53 crore but this was subsequently revised to Rs. 2671440.77 crore implying a cost overrun of 19.6%. The expenditure incurred on these projects till April, 2021 is Rs. 1316032.62 crore, which is 49.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

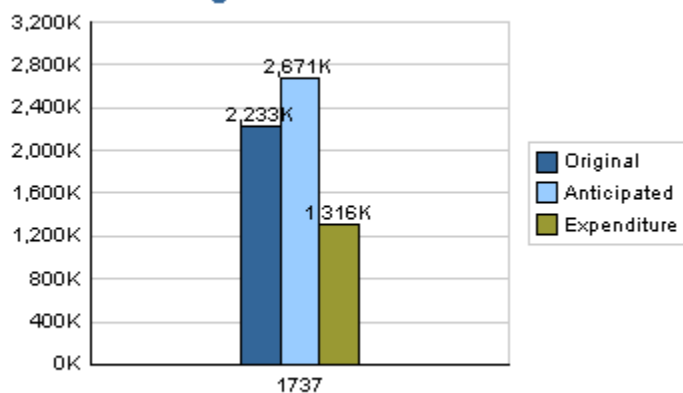

Sector wise current status of projects on the Flash Report


DPIIT

Current Status:

Number of Projects	2
Number of Projects Delayed	2

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 2 projects are delayed.




Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 17352.09 crore but this was subsequently anticipated to Rs. 18990.3 crore implying a cost overrun of 9.4%. The expenditure incurred on these projects till April, 2021 is Rs. 11472.42 crore, which is 60.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

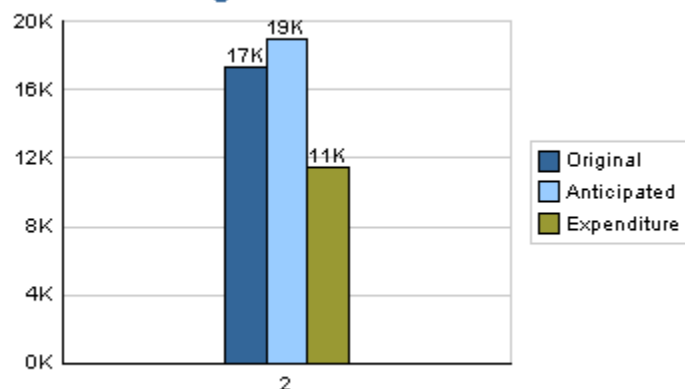

Sector wise current status of projects on the Flash Report


RURAL DEVELOPMENT

Current Status:

Number of Projects	4
Number of Projects On Schedule	1
Number of Projects Delayed	3

Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 1 project is on schedule 3 projects are delayed.

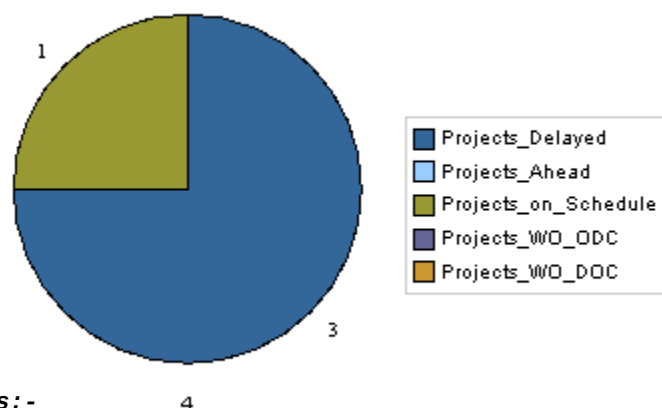


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 889.43 crore but this was subsequently anticipated to Rs. 899.87 crore implying a cost overrun of 1.2%. The expenditure incurred on these projects till April, 2021 is Rs. 472.48 crore, which is 52.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

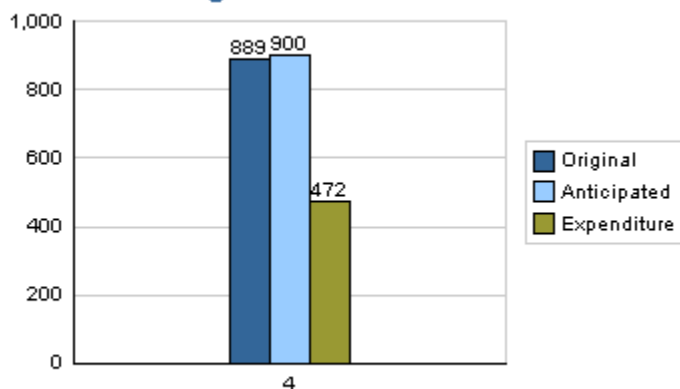

Sector wise current status of projects on the Flash Report


HOME AFFAIRS

Current Status:

Number of Projects	5
Number of Projects On Schedule	3
Number of Projects Delayed	2

Brief Analysis

Project Status with respect to Original Schedule: Out of 5 projects, 3 projects are on schedule 2 projects are delayed.

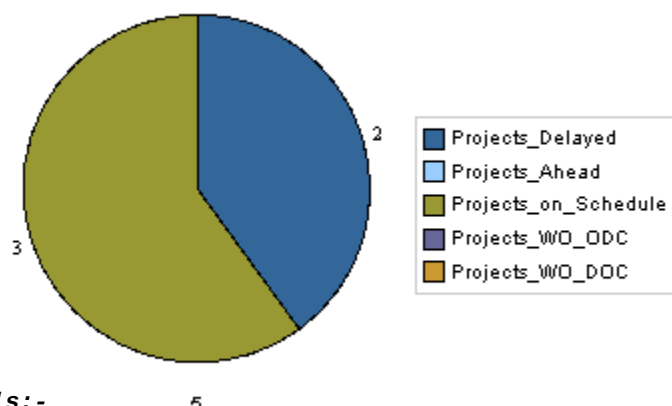


Total No Of Project's:-

5

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 1993.4 crore but this was subsequently anticipated to Rs. 2849.31 crore implying a cost overrun of 42.9%. The expenditure incurred on these projects till April, 2021 is Rs. 1088.12 crore, which is 38.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

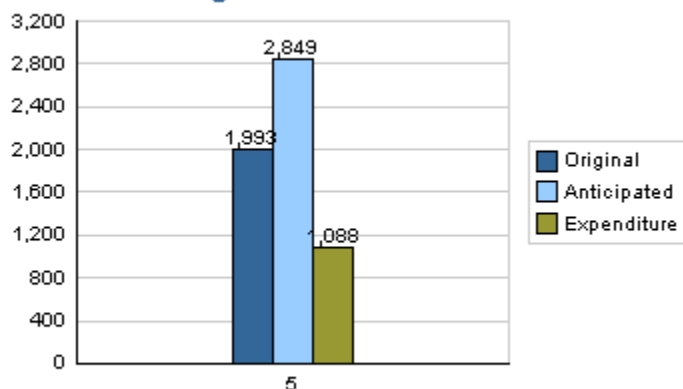

Sector wise current status of projects on the Flash Report

HUMAN RESOURCE DEVELOPMENT


Current Status:

Number of Projects	26
Number of Projects On Schedule	4
Number of Projects Delayed	12

Number of Projects Without Date Of Commissioning 10

Brief Analysis

Project Status with respect to Original Schedule: Out of 26 projects, 4 projects are on schedule 12 projects are delayed. 10 projects do not have fixed dates of commissioning.

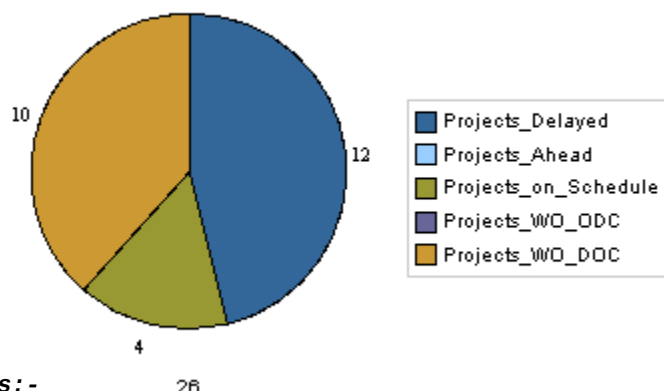


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 26 projects when sanctioned, was of the order of Rs. 11077.4 crore but this was subsequently anticipated to Rs. 11265.83 crore implying a cost overrun of 1.7%. The expenditure incurred on these projects till April, 2021 is Rs. 2475.25 crore, which is 22% of the anticipated cost of the projects.

Figures are in Rs. Crore

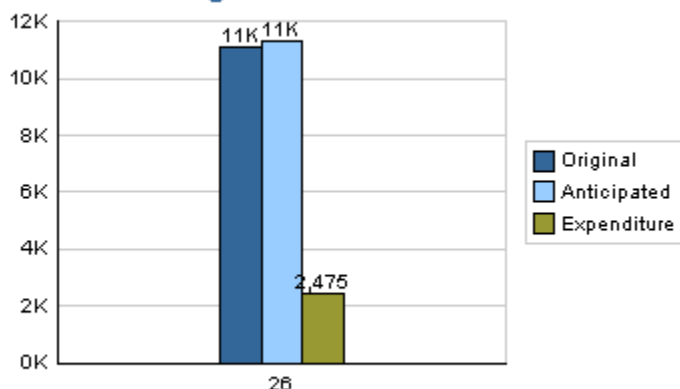

Sector wise current status of projects on the Flash Report

WATER RESOURCES


Current Status:

Number of Projects	49
Number of Projects On Schedule	24
Number of Projects Delayed	13

Number of Projects Without Date Of Commissioning	12
--	----

Brief Analysis

Project Status with respect to Original Schedule: Out of 49 projects, 24 projects are on schedule 13 projects are delayed. 12 projects do not have fixed dates of commissioning.

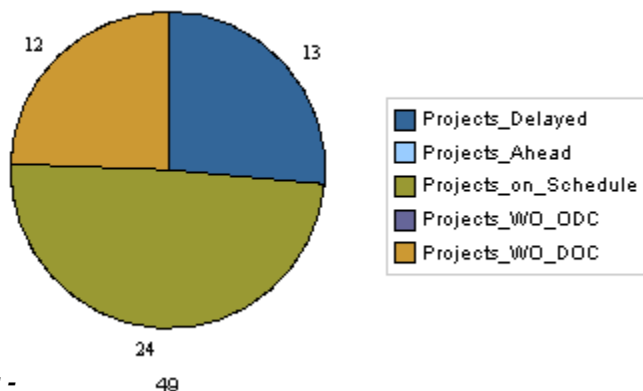


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 49 projects when sanctioned, was of the order of Rs. 26781.06 crore but this was subsequently anticipated to Rs. 72049.94 crore implying a cost overrun of 169%. The expenditure incurred on these projects till April, 2021 is Rs. 22138.4 crore, which is 30.7% of the anticipated cost of the projects.

Figures are in Rs. Crore

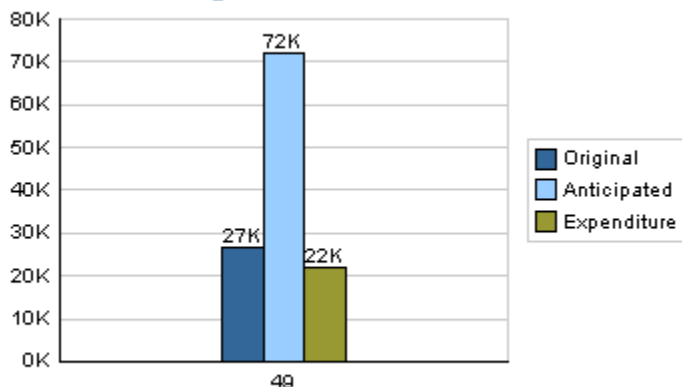

Sector wise current status of projects on the Flash Report


TELECOMMUNICATIONS

Current Status:

Number of Projects	3
Number of Projects Delayed	3

Brief Analysis

Project Status with respect to Original Schedule: Out of 3 projects, 3 projects are delayed.

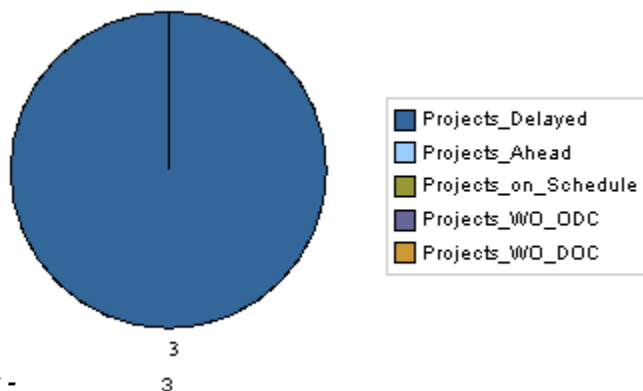


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 3 projects when sanctioned, was of the order of Rs. 14013.36 crore but this was subsequently anticipated to Rs. 25343.36 crore implying a cost overrun of 80.9%. The expenditure incurred on these projects till April, 2021 is Rs. 17990.26 crore, which is 71% of the anticipated cost of the projects.

Figures are in Rs. Crore

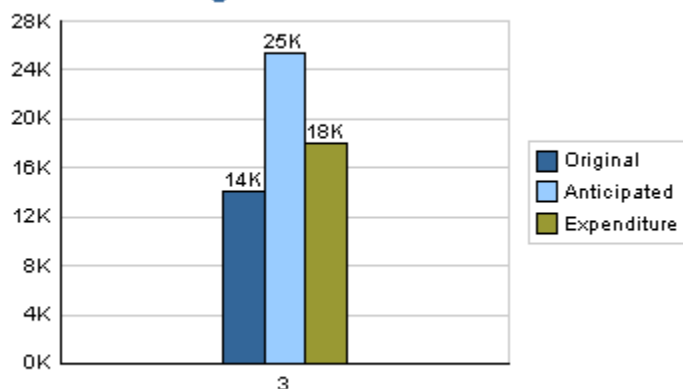

Sector wise current status of projects on the Flash Report

ROAD TRANSPORT AND HIGHWAYS


Current Status:

Number of Projects	908
Number of Projects On Schedule	54
Number of Projects Delayed	118

Number of Projects Without Original Date of Commissioning	52
Number of Projects Without Date Of Commissioning	684

Brief Analysis

Project Status with respect to Original Schedule: Out of 908 projects, 54 projects are on schedule 118 projects are delayed. 684 projects do not have fixed dates of commissioning. 52 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

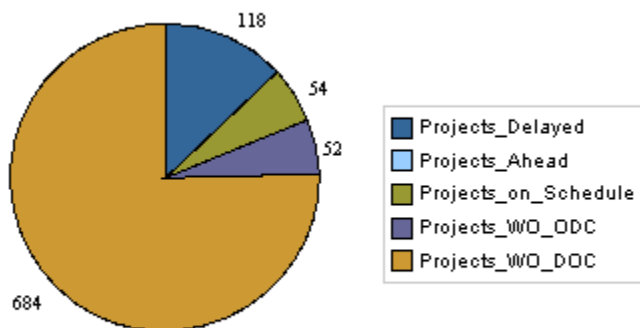


Total No Of Project's:-

908

Investment Scenario

Total original cost of implementation of 908 projects when sanctioned, was of the order of Rs. 540947.36 crore but this was subsequently anticipated to Rs. 561176 crore implying a cost overrun of 3.7%. The expenditure incurred on these projects till April, 2021 is Rs. 351797.31 crore, which is 62.7% of the anticipated cost of the projects.

Figures are in Rs. Crore

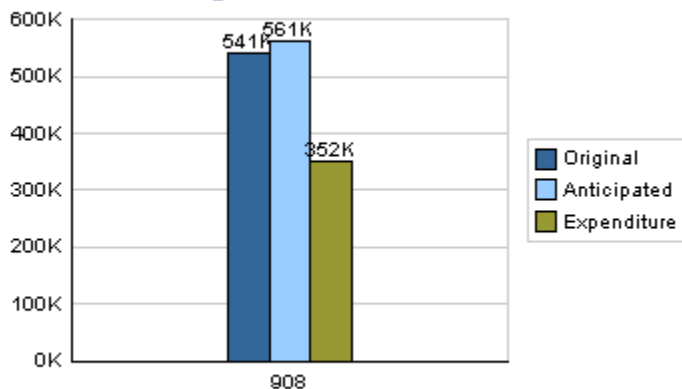

Sector wise current status of projects on the Flash Report

RAILWAYS


Current Status:

Number of Projects	312
Number of Projects On Schedule	14
Number of Projects Delayed	148
Number of Projects Ahead	5
Number of Projects Without Original Date of Commissioning	46
Number of Projects Without Date Of Commissioning	99

Brief Analysis

Project Status with respect to Original Schedule: Out of 312 projects, 5 projects are ahead of schedule, 14 projects are on schedule 148 projects are delayed. 99 projects do not have fixed dates of commissioning. 46 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.


Total No Of Project's:-

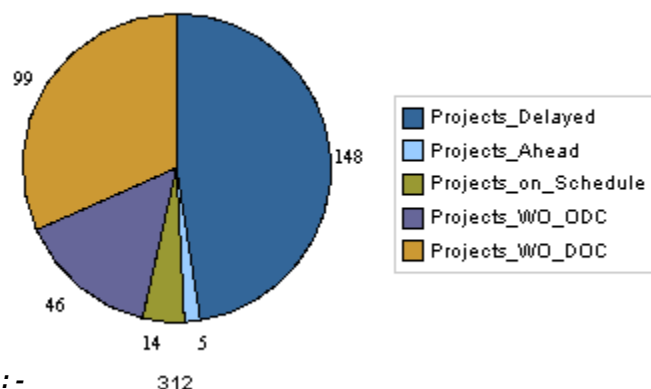

Investment Scenario

Total original cost of implementation of 312 projects when sanctioned, was of the order of Rs. 462095.03 crore but this was subsequently anticipated to Rs. 700076.37 crore implying a cost overrun of 51.5%. The expenditure incurred on these projects till April, 2021 is Rs. 250483.48 crore, which is 35.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

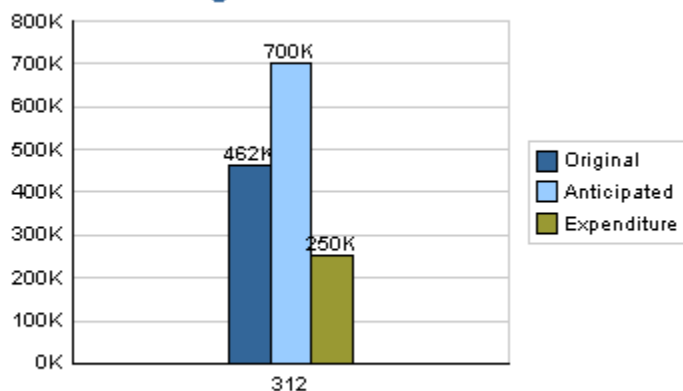

Sector wise current status of projects on the Flash Report


HEALTH AND FAMILY WELFARE

Current Status:

Number of Projects	29
Number of Projects On Schedule	3
Number of Projects Delayed	10
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	4
Number of Projects Without Date Of Commissioning	11

Brief Analysis

Project Status with respect to Original Schedule: Out of 29 projects, 1 project is ahead of schedule, 3 projects are on schedule 10 projects are delayed. 11 projects do not have fixed dates of commissioning. 4 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

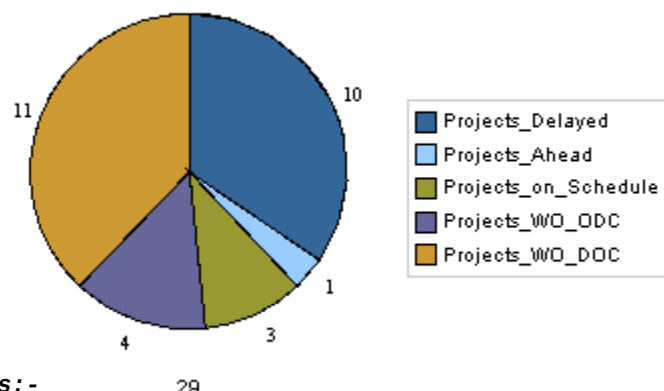


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 29 projects when sanctioned, was of the order of Rs. 15273.26 crore but this was subsequently anticipated to Rs. 15628.51 crore implying a cost overrun of 2.3%. The expenditure incurred on these projects till April, 2021 is Rs. 7898.83 crore, which is 50.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

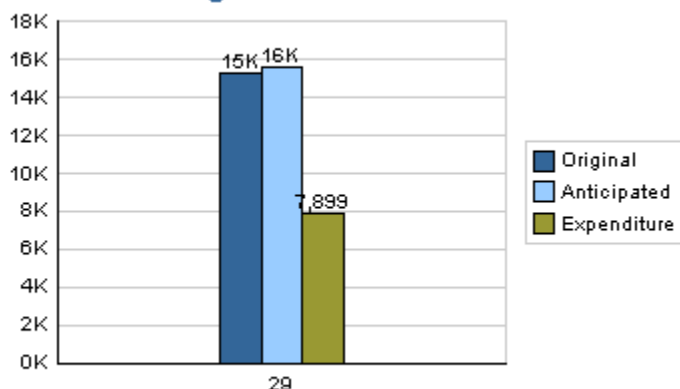

Sector wise current status of projects on the Flash Report

POWER


Current Status:

Number of Projects	78
Number of Projects On Schedule	7
Number of Projects Delayed	43

Number of Projects Without Date Of Commissioning 28

Brief Analysis

Project Status with respect to Original Schedule: Out of 78 projects, 7 projects are on schedule 43 projects are delayed. 28 projects do not have fixed dates of commissioning.

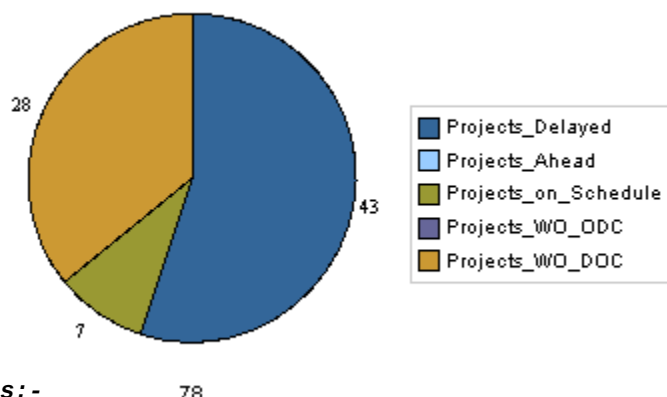


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 78 projects when sanctioned, was of the order of Rs. 295137.42 crore but this was subsequently anticipated to Rs. 367699.63 crore implying a cost overrun of 24.6%. The expenditure incurred on these projects till April, 2021 is Rs. 256834.13 crore, which is 69.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

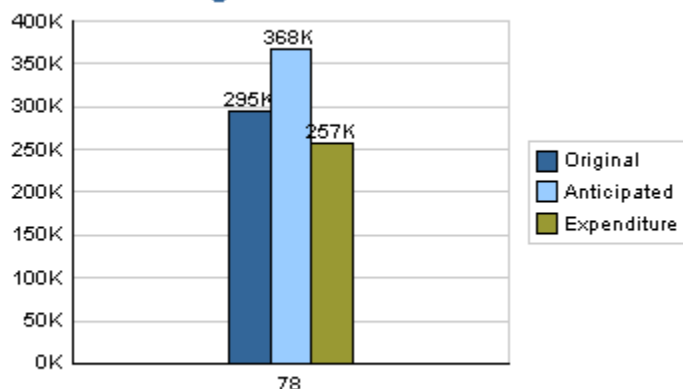

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	139
Number of Projects On Schedule	47
Number of Projects Delayed	78
Number of Projects Ahead	5
Number of Projects Without Original Date of Commissioning	2
Number of Projects Without Date Of Commissioning	7

Brief Analysis

Project Status with respect to Original Schedule: Out of 139 projects, 5 projects are ahead of schedule, 47 projects are on schedule 78 projects are delayed. 7 projects do not have fixed dates of commissioning. 2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

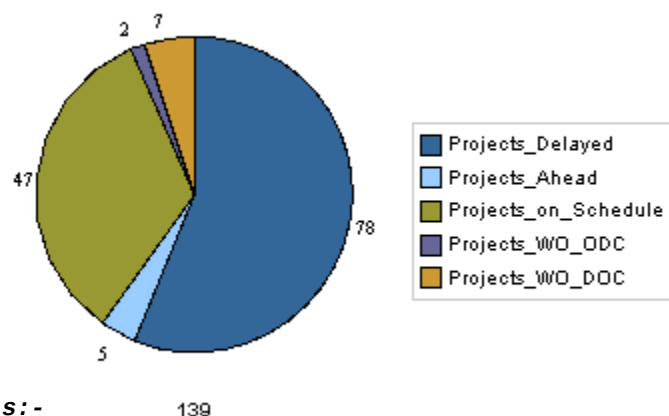


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 139 projects when sanctioned, was of the order of Rs. 296976.45 crore but this was subsequently anticipated to Rs. 304256.68 crore implying a cost overrun of 2.5%. The expenditure incurred on these projects till April, 2021 is Rs. 115047.73 crore, which is 37.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

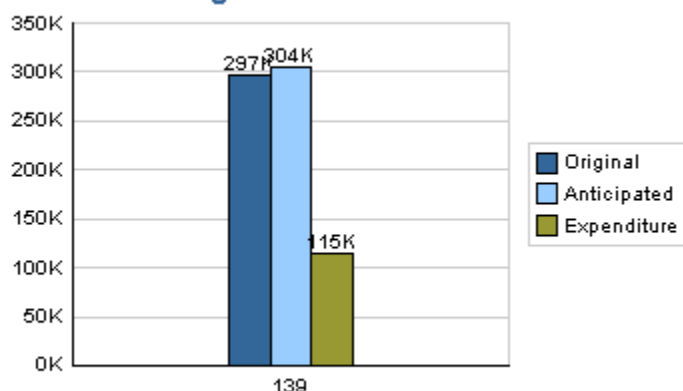

Sector wise current status of projects on the Flash Report


STEEL

Current Status:

Number of Projects	9
Number of Projects On Schedule	3
Number of Projects Delayed	6

Brief Analysis

Project Status with respect to Original Schedule: Out of 9 projects, 3 projects are on schedule 6 projects are delayed.

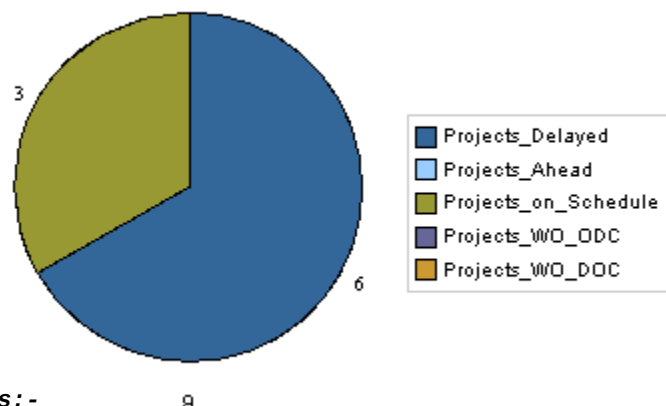


Total No Of Project's:-

9

Investment Scenario

Total original cost of implementation of 9 projects when sanctioned, was of the order of Rs. 25452.51 crore but this was subsequently anticipated to Rs. 31567.51 crore implying a cost overrun of 24%. The expenditure incurred on these projects till April, 2021 is Rs. 23179.8 crore, which is 73.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

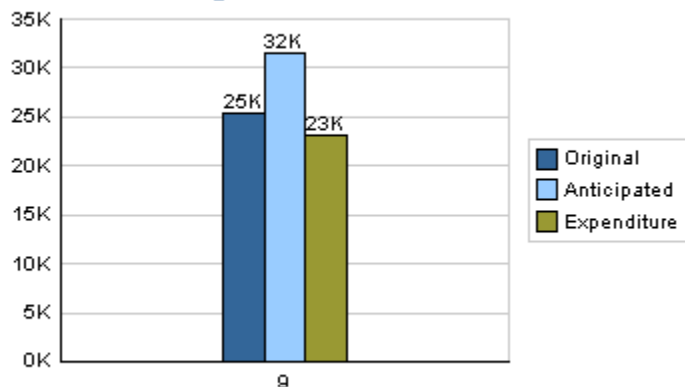

Sector wise current status of projects on the Flash Report

MINES

Current Status:


Number of Projects **5**

Number of Projects Delayed **2**

Number of Projects Without Date Of Commissioning **3**

Brief Analysis

Project Status with respect to Original Schedule: Out of 5 projects, 2 projects are delayed. 3 projects do not have fixed dates of commissioning.

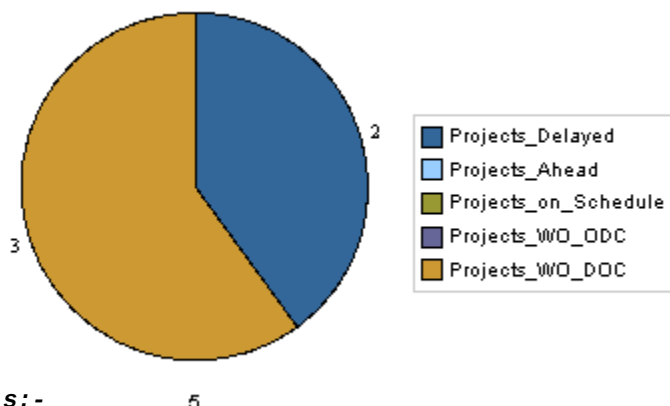


Total No Of Project's:-

5

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 7078.62 crore but this was subsequently anticipated to Rs. 7075.17 crore. The expenditure incurred on these projects till April, 2021 is Rs. 1301.06 crore, which is 18.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

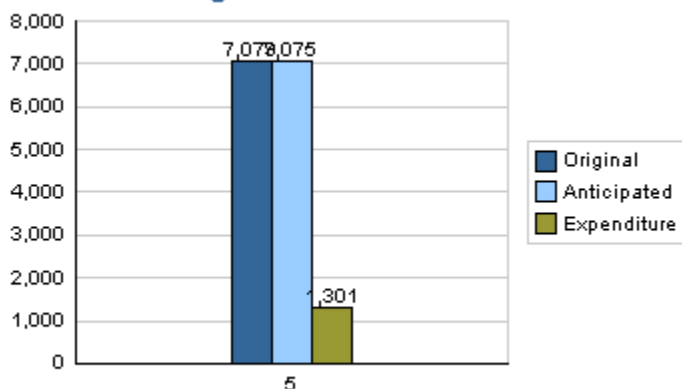

Sector wise current status of projects on the Flash Report


FERTILISERS

Current Status:

Number of Projects	4
Number of Projects Delayed	4

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed.

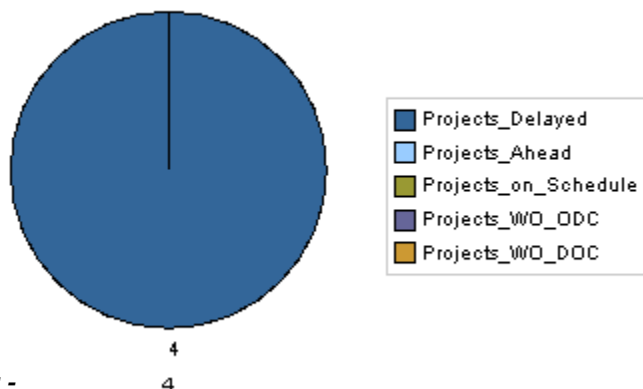

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 1101.28 crore but this was subsequently anticipated to Rs. 1101.28 crore. The expenditure incurred on these projects till April, 2021 is Rs. 847.51 crore, which is 77% of the anticipated cost of the projects.

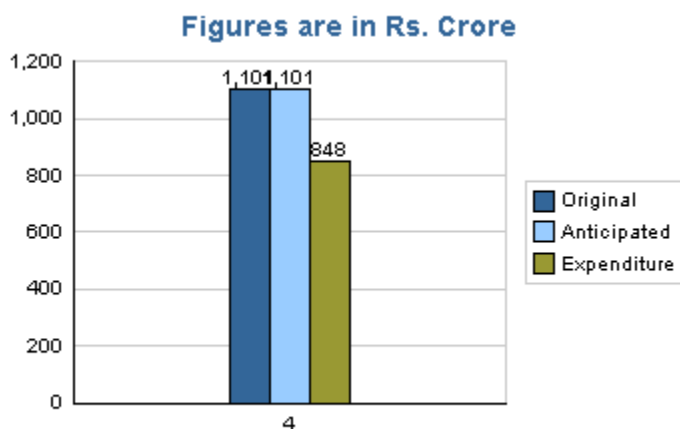

Sector wise current status of projects on the Flash Report

COAL


Current Status:

Number of Projects	101
Number of Projects On Schedule	35
Number of Projects Delayed	52

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	13

Brief Analysis

Project Status with respect to Original Schedule: Out of 101 projects, 35 projects are on schedule 52 projects are delayed. 13 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

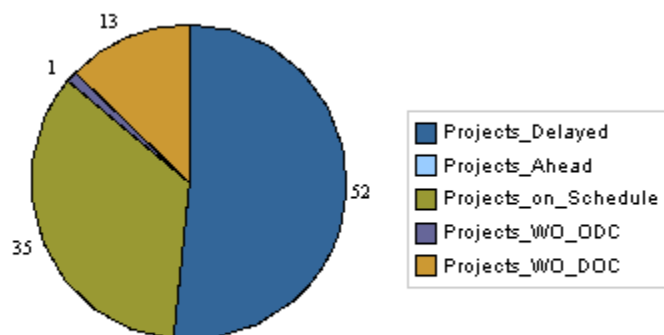


Total No Of Project's:-

101

Investment Scenario

Total original cost of implementation of 101 projects when sanctioned, was of the order of Rs. 145653.01 crore but this was subsequently anticipated to Rs. 144995 cr The expenditure incurred on these projects till April, 2021 is Rs. 49331.74 crore, which is 34% of the anticipated cost of the projects.

Figures are in Rs. Crore

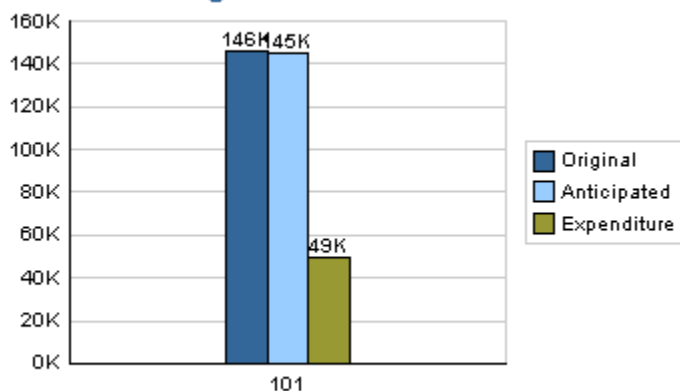

Sector wise current status of projects on the Flash Report


CIVIL AVIATION

Current Status:

Number of Projects	19
Number of Projects On Schedule	5
Number of Projects Delayed	14

Brief Analysis

Project Status with respect to Original Schedule: Out of 19 projects, 5 projects are on schedule 14 projects are delayed.

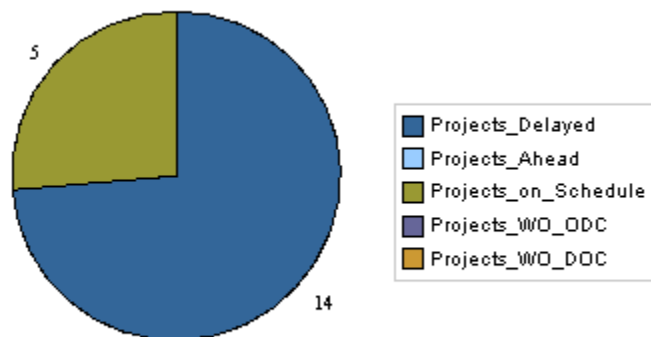


Total No Of Project's:-

19

Investment Scenario

Total original cost of implementation of 19 projects when sanctioned, was of the order of Rs. 13786.34 crore but this was subsequently anticipated to Rs. 14264.62 crore implying a cost overrun of 3.5%. The expenditure incurred on these projects till April, 2021 is Rs. 4197.34 crore, which is 29.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

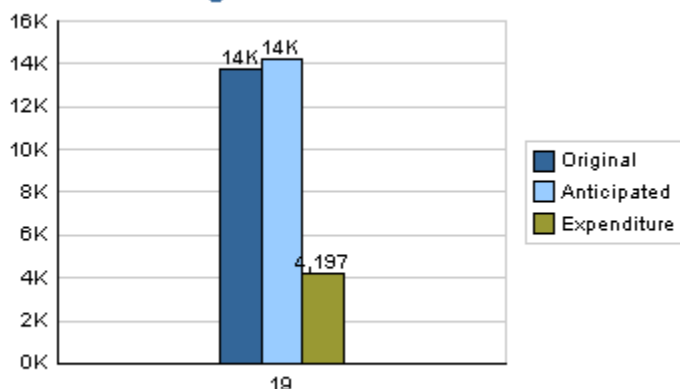

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	4

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed.

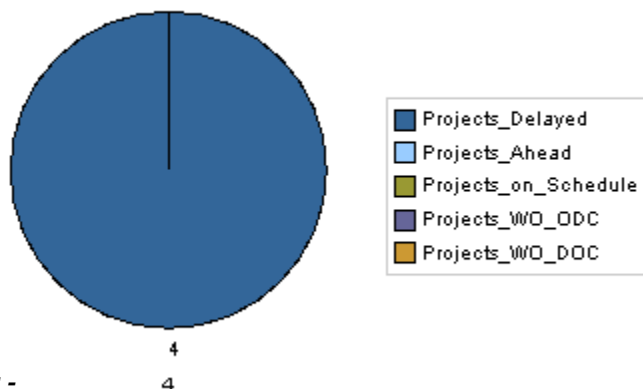

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 67120 crore but this was subsequently anticipated to Rs. 80348 crore implying a cost overrun of 19.7%. The expenditure incurred on these projects till April, 2021 is Rs. 59554.96 crore, which is 74.1% of the anticipated cost of the projects.

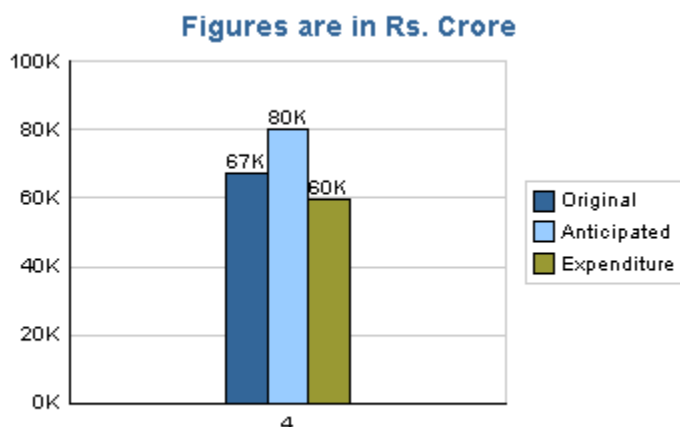

Annexure - I

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE (APRIL 2021)

(All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	A & N ISLANDS	9	2,888.63	3,159.99	786.13
2	ANDHRA PRADESH	77	1,22,880.98	1,70,411.65	75,650.82
3	ARUNACHAL PRADESH	42	24,624.65	44,366.68	27,514.89
4	ASSAM	47	42,046.33	45,563.88	14,553.02
5	BIHAR	108	1,22,099.62	1,58,462.5	76,045.65
6	CHANDIGARH	2	349.15	570	270.91
7	CHHATISGARH	48	91,239.04	1,02,416.44	57,621.69
8	DELHI	36	90,723.12	92,153.92	55,981.08
9	GOA	11	5,629.77	5,640.26	2,596.62
10	GUJARAT	59	1,06,069.6	1,17,304.95	57,845.7
11	HARYANA	43	30,316.35	32,837.14	18,841.47
12	HIMACHAL PRADESH	15	20,365.24	30,249.67	17,671.88
13	JAMMU AND KASHMIR	22	40,412.13	66,473.44	43,047.03
14	JHARKHAND	42	70,673.4	68,776.1	33,999.89
15	KARNATAKA	60	71,320.53	80,896.72	42,649.32
16	KERALA	22	37,466.85	42,584.93	19,544.87
17	MADHYA PRADESH	84	91,161.4	1,04,808.86	55,571.41
18	MAHARASHTRA	242	2,17,334.38	2,41,218.69	1,34,708.13
19	MANIPUR	12	8,137.49	15,887.67	11,322.77
20	MEGHALAYA	7	3,245.09	6,563.59	1,519.29
21	MIZORAM	18	9,030.03	12,978.73	6,394.66
22	MULTI STATE	128	3,66,425.54	4,81,291.29	1,92,078.21
23	NAGALAND	38	18,265.97	22,463.91	4,426.19
24	ODISHA	89	1,29,891.78	1,34,147.04	56,652.18
25	PONDICHERRY	1	195	195	16.41
26	PUNJAB	29	15,325.05	18,249.98	11,102.59
27	RAJASTHAN	60	53,090.5	61,137.54	39,988.28
28	SIKKIM	14	5,074.99	12,994.31	1,896.5
29	TAMIL NADU	71	1,19,185.26	1,38,369.59	81,621.86
30	TELANGANA	47	36,326.25	39,359.69	19,894.41
31	TRIPURA	13	3,479.87	3,626.4	1,481.78
32	UTTAR PRADESH	134	1,78,012.58	1,85,467.12	91,848.45
33	UTTARAKHAND	32	34,539.29	46,325.58	15,403.33
34	WEST BENGAL	75	65,583.67	84,487.51	45,485.2
TOTAL		1,737	22,33,409.53	26,71,440.77	13,16,032.62

Details of Projects Ahead of Schedule w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>FERTILISERS</u>						
	<u>National Fertiliser Limited</u>						
1	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014	1/2018	215.92 -	215.92	168.30	11/2019 06/2021	05/2021
2	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015	1/2018	218.83 -	218.83	191.30	11/2019 05/2021	04/2021
3	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016	1/2018	239.81 -	239.81	199.11	11/2019 05/2021	04/2021
	Total		674.56 -	674.56	558.71		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Central Public Works Department</u>						
4	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150	3/2019	1,828.00	1,828.00	-	09/2025 -	05/2024
	Total		1,828.00 -	1,828.00	.00		
	<u>PETROLEUM</u>						
	<u>Gas Authority Of India Limited</u>						
5	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273	3/2017	2,433.00 -	2,433.00	2,110.70	12/2020 12/2021	06/2021
	<u>Hindustan Petroleum Corporation Limited</u>						
6	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315	6/2017	249.26 -	249.26	134.44	06/2020 12/2021	09/2021
	<u>Indian Oil Corporation Limited</u>						
7	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308	8/2017	315.00 -	315.00	208.09	12/2021 -	08/2021
8	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI - [N16000405	10/2020	1,398.00 -	1,398.00	80.68	12/2023 -	05/2023
9	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332	3/2018	3,712.00 -	3,696.00	1,995.95	09/2022 -	03/2022
	Total		8,107.26 -	8,091.26	4,529.86		
	<u>POWER</u>						
	<u>Power Grid Corporation Of India Limited</u>						
10	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164	5/2014	522.29 546.36	546.36	478.29	11/2016 09/2021	06/2021
11	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244	2/2017	235.53 -	235.53	151.12	06/2019 08/2021	06/2021

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		757.82	781.89	629.41		
			-				
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
12	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	2/2015	3,627.47	3,627.47	1,204.21	03/2024	03/2023
	<u>Metropolitan Rapid Transport Projects</u>						
13	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	4/2006	495.74	734.01	510.69	06/2013 06/2022	12/2021
	<u>North East Frontier Railway</u>						
14	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	4/2016	602.27	2,144.78	921.83	12/2021	04/2021
	<u>Rail Vikas Nigam Ltd.</u>						
15	BHANUPALI-BILASPUR BERI NL - [N22000273]	4/2008	2,966.99	6,753.42	926.84	12/2026	12/2025
			-				
16	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78	723.78	.19	12/2025	03/2025
			-				
17	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	4/2010	2,127.00	3,000.00	2,208.46	03/2023	12/2022
			-				
	<u>South Central Railway</u>						
18	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	4/2010	704.31	927.94	534.34	03/2020 03/2022	06/2021
	<u>Southern Railway</u>						
19	MADURAI-BODINAYAKKANUR - [N22000201]	4/2008	164.41	608.13	375.67	- 10/2021	09/2021
	<u>West Central Railway</u>						
20	RAMGANJMUNDI-BHOPAL (NL), WCR - [220100314]	4/2001	424.60	2,909.99	1,229.79	03/2021 03/2029	03/2023
	Total		11,836.57	21,429.52	7,912.02		
			-				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>National Highways Authority Of India</u>						
21	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]	11/2016	1,064.88	1,021.00	336.32	- 01/2022	07/2021
			-				
22	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]	3/2018	1,532.62	2,499.00	761.73	03/2021 10/2021	04/2021
			-				
	Total		2,597.50	3,520.00	1,098.05		
			-				
	<u>WATER RESOURCES</u>						
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>						
23	I AND D AND STP AT CHAPPRA - [N30000028]	11/2018	236.15	236.15	46.50	12/2020 06/2021	04/2021
			-				
	Total		236.15	236.15	46.50		
			-				

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	Grand Total		26,037.86	36,561.38	14,774.55		

Details of Projects Without Original Date of Commissioning

Annexure - IX

Costing Rs. 150 Crore and above (April 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>COAL</u>								
	<u>Singareni Colliers Company Limited</u>								
1	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL, TELANGANA	11/2016	272.73	272.73	153.75	-	03/2022	-	2/6
	Total		272.73	272.73	153.75				2/6
	<u>PETROLEUM</u>								
	<u>Indian Oil Corporation Limited</u>								
2	LPG BP PROJECT JODHPUR - [N16000318]IOCL, RAJASTHAN	03/2018	229.80	229.80	81.48	-	05/2022	0(R3)	17/26
3	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT - [N16000336]IOCL, GUJARAT	03/2018	588.20	730.20	77.30	-	05/2023	0(R3)	12/17
	Total		818.00	960.00	158.78				29/43
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Hospital Services Consultancy Corporation Ltd</u>								
4	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC, DELHI	12/2017	156.56	190.34	143.14	-	06/2021	-	0/0
5	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC, ANDHRA PRADESH	03/2018	601.02	601.02	400.25	-	06/2021	-	0/0
6	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC, MAHARASHTRA	03/2018	582.99	582.99	482.32	-	06/2021	-	0/0
7	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC, WEST BENGAL	04/2018	651.99	651.99	503.55	-	06/2021	-	0/0
	Total		1,992.56	2,026.34	1,529.26				0/0
	<u>RAILWAYS</u>								
	<u>East Central Railways</u>								
8	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR, JHARKHAND	03/1999	1,033.07	3,550.00	3,567.20	-	03/2022	-	0/0
9	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIAWAN-BIHARSHARIF, - [N22000476]ECR, BIHAR	04/1991	329.39	1,483.14	1,207.52	-	03/2022	-	0/0
10	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR, BIHAR	04/2003	528.65	2,066.78	1,560.44	-	03/2023	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (April 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
11	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	1,625.87	758.44	- -	03/2023	-	0/0
12	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR	04/2006	378.56 -	1,858.75	386.35	- -	03/2023	-	0/0
13	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	1,605.17 -	1,605.17	53.52	- -	03/2023	-	0/0
14	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	1,470.50	1,288.24	- -	03/2023	-	0/0
15	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	614.45	348.95	- -	12/2023	-	0/0
16	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR	04/2008	326.20 -	2,995.01	2.08	- -	03/2024	-	0/0
17	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	228.05	1.53	- -	03/2024	-	0/0
18	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	519.33	282.65	- -	03/2025	-	0/0
	<u>Eastern Railways</u>								
19	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	495.10	288.51	- -	03/2022	-	0/0
20	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64 -	272.20	261.26	- -	03/2022	-	0/0
21	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	310.70	293.10	- -	03/2024	-	0/0
22	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	1,261.34	-	- -	03/2025	-	0/0
23	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	260.10	11.74	- -	03/2025	-	0/0
24	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	174.56	71.43	- -	03/2025	-	0/0
25	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	250.55	20.11	- -	03/2025	-	0/0
26	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	527.54	1.76	- -	03/2025	-	0/0
27	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	298.22	52.09	- -	03/2025	-	0/0
28	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	336.96	70.20	- -	03/2025	-	0/0
29	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGREGATION OF ARRIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	166.89	.02	- -	03/2025	-	0/0
	<u>Metropolitan Rapid Transport Projects</u>								

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (April 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
30	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	268.52	.03	- -	03/2025	-	0/0
	<u>North East Frontier Railway</u>								
31	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR, MULTI STATE	04/2010	241.52 -	373.87	287.09	- -	12/2021	-	0/0
	<u>North Eastern Railway</u>								
32	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER, UTTAR PRADESH	04/2016	602.50 -	714.34	40.34	- -	12/2023	-	0/0
	<u>Northern Railway</u>								
33	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR, MULTI STATE	04/2007	336.91 -	791.39	572.99	- -	03/2023	-	0/0
34	UNCHAHAR-AMETHI - [N22000294]NR, UTTAR PRADESH	04/2012	1,229.00 -	1,265.00	103.72	- -	03/2023	-	0/0
35	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR, DELHI	04/2012	295.68 -	419.00	127.91	- -	09/2023	-	0/0
36	GRADE SEPARATOR AT DAYABASTI - [N22000269]NR, DELHI	04/1999	156.65 -	359.00	111.51	- -	03/2024	-	0/0
37	QADIAN-BEAS - [N22000295]NR, PUNJAB	04/2011	205.22 -	841.90	1.73	- -	03/2024	-	0/0
	<u>South Eastern Railway</u>								
38	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	620.00	40.99	- -	03/2025	-	0/0
	<u>South Western Railway</u>								
39	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR, KARNATAKA	04/2011	1,801.01 -	1,967.00	71.56	- -	12/2023	-	0/0
40	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR, KARNATAKA	04/2013	558.00 -	558.00	-	- -	12/2023	-	0/0
41	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR, MULTI STATE	04/2013	296.00 -	296.10	.01	- -	12/2023	-	0/0
42	WHITE FIELD-KOLAR NL - [N22000280]SWR, KARNATAKA	04/2011	348.85 -	348.85	.36	- -	12/2023	-	0/0
43	TORANAGALLU-RANJITPURA DL - [N22000298]SWR, KARNATAKA	04/2011	146.75 -	167.50	.34	- -	12/2023	-	0/0
44	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR, KARNATAKA	04/2013	327.25 -	327.25	-	- -	12/2023	-	0/0
45	HUBLI-ANKOLA(NL), SWR - [220100193]SWR, KARNATAKA	04/1997	2,315.00 -	3,911.65	157.01	- -	12/2024	-	0/0
46	RAYADURGA-TUMKUR NL - [N22000279]SWR, MULTI STATE	04/2007	2,062.30 -	2,432.50	1,127.71	- -	03/2025	-	2/2
	<u>Southern Railway</u>								
47	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR, TAMIL NADU	04/2007	931.98 -	1,121.00	928.75	- 05/2021	05/2021	0(R3)	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (April 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
48	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	608.13	375.67	- 10/2021	09/2021	-1(R3)	0/0
49	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	457.08	439.49	- -	12/2021	-	0/0
50	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	1,205.00	2.28	- -	03/2024	-	0/0
51	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	559.95	52.50	- -	03/2024	-	0/0
52	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	582.83	239.49	- -	12/2025	-	0/0
	<u>Western Railway</u>								
53	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	844.10 844.10	844.10	186.59	- 03/2024	03/2024	0(R3)	0/0
	Total		24,180.46 -	43,411.17	15,395.21				2/2
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>								
54	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]MoRTH,CHHATISGARH	12/2015	291.05 -	291.05	212.46	- 06/2021	06/2021	0(R3)	0/0
55	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH,MADHYA PRADESH	06/2015	390.51 -	390.51	257.01	- 03/2021	06/2021	3(R3)	0/0
56	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH	11/2016	326.99 327.00	326.99	105.89	- -	09/2021	-	0/0
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
57	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA	04/2017	553.51 -	553.51	75.51	- -	09/2021	-	2/4
58	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH	02/2017	175.06 -	175.06	82.18	- -	04/2022	-	2/4
59	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL,ARUNACHAL PRADESH	02/2017	176.12 -	176.12	67.95	- -	04/2022	-	2/4
	<u>National Highways Authority Of India</u>								
60	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA	03/2018	806.11 -	806.11	189.70	- -	04/2021	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (April 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
61	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI, GUJARAT	05/2016	364.56 -	392.00	353.42	- -	04/2021	-	0/0
62	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI, MAHARASHTRA	01/2018	621.00 -	621.00	591.21	- -	04/2021	-	2/3
63	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT (APP - [N24000624]NHAI, MULTI STATE	09/2016	1,244.10 -	1,244.10	1,590.00	- -	05/2021	-	0/0
64	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI, HIMACHAL PRADESH	03/2018	478.74 -	478.74	127.42	- -	05/2021	-	0/0
65	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI, ODISHA	10/2016	1,008.96 -	1,008.96	930.39	- -	06/2021	-	0/0
66	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI, ODISHA	12/2017	686.65 -	686.65	227.63	- -	06/2021	-	0/0
67	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI, ODISHA	12/2017	417.51 -	417.51	127.61	- -	06/2021	-	0/0
68	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI, ODISHA	01/2018	668.86 -	668.86	276.59	- -	06/2021	-	0/0
69	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI, ODISHA	01/2018	686.65 -	686.65	261.74	- -	06/2021	-	0/0
70	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK - [N24000737]NHAI, ODISHA	01/2018	1,522.00 -	1,522.00	304.40	- -	06/2021	-	0/0
71	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI, ODISHA	01/2018	999.00 -	999.00	102.70	- -	06/2021	-	0/0
72	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI, ODISHA	01/2018	503.88 -	503.88	25.40	- -	06/2021	-	0/0
73	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI, GUJARAT	03/2018	2,702.05 -	2,043.00	1,327.65	- -	06/2021	-	0/0
74	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI, PUNJAB	09/2014	479.00 -	479.00	456.80	- -	07/2021	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (April 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
75	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA	11/2016	1,071.61 -	1,048.10	965.72	- -	07/2021	-	3/4
76	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA	11/2016	1,064.88 -	1,021.00	336.32	- 01/2022	07/2021	-6(R3)	1/4
77	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	1,323.15	785.33	- -	07/2021	-	0/0
78	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI,WEST BENGAL	03/2018	1,261.98 -	1,952.20	934.06	- -	07/2021	-	0/0
79	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB	02/2018	261.76 -	207.00	200.74	- -	07/2021	-	0/0
80	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64 -	1,437.64	564.11	- -	07/2021	-	0/0
81	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA	03/2018	634.70 -	931.21	268.17	- -	07/2021	-	0/0
82	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA	03/2018	795.50 -	799.30	213.17	- -	07/2021	-	0/0
83	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 -	1,162.92	58.20	- -	07/2021	-	0/0
84	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27 -	950.27	224.81	- -	08/2021	-	3/4
85	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA	01/2018	607.00 -	607.00	440.92	- -	08/2021	-	0/1
86	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	614.48	217.40	- -	08/2021	-	0/0
87	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	564.66	240.00	- -	08/2021	-	0/1
88	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26 -	1,296.93	220.78	- -	08/2021	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (April 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
89	FOUR LANING OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35 -	505.35	243.30	- -	08/2021	-	0/0
90	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21 -	289.21	194.57	- 02/2021	08/2021	6(R3)	0/0
91	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	1,031.95	374.05	- -	09/2021	-	0/0
92	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 -	1,550.98	1,401.00	- -	09/2021	-	0/0
93	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	825.17	512.04	- -	10/2021	-	2/4
94	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 -	1,959.00	1,211.72	- -	10/2021	-	0/0
95	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 -	2,400.00	3,088.59	- -	11/2021	-	0/0
96	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	1,117.84	-	- -	12/2021	-	0/0
97	FOUR LANING OF MADURAI- CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	628.71	310.06	- -	12/2021	-	0/0
98	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI,MADHYA PRADESH	10/2019	743.88 -	743.89	298.54	- -	12/2021	-	0/3
99	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU	03/2018	1,016.92 -	1,071.00	218.47	- -	01/2022	-	0/0
100	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53 -	291.53	150.06	- 08/2021	02/2022	6(R3)	0/0
101	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA - [N24001213]NHAI,MADHYA PRADESH	12/2017	1,094.97 -	1,094.97	-	- -	02/2022	-	2/4
102	FOUR LANING WITH PS TALEBANI - SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	752.28	213.52	- -	03/2022	-	0/1

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (April 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
103	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	953.09	332.04	- -	03/2022	-	0/0
104	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43 -	314.43	85.61	- -	03/2022	-	0/0
105	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]NHAI,MADHYA PRADESH	12/2017	656.98 -	840.00	105.50	- -	11/2022	-	0/4
	Total		43,735.62 -	44,755.96	22,102.46				19/45
	<u>URBAN DEVELOPMENT</u>								
	<u>National Building Construcion Corporation Ltd</u>								
106	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI	07/2016	2,694.00 -	2,694.00	744.73	- -	12/2022	-	0/9
	Total		2,694.00 -	2,694.00	744.73				0/9
	Grand Total		73,693.37	94,120.20	40,084.19				52/105

Details of Projects Without Date of Commissioning

Annexure - VIII

Costing Rs. 150 Crore and above				(April 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>COAL</u>				
	<u>Bharat Coking Coal Limited</u>				
1	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	04/2014 -	04/2020
2	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND	02/2014	555.52 -	03/2021 -	-
	<u>Eastern Coal Fields Limited</u>				
3	RANIGANJ MASTER PLAN - [N06000163]ECL, WEST BENGAL	08/2009	2,661.73 -	08/2019 -	-
	<u>Mahanadi Coal Fields Limited</u>				
4	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL, ODISHA	08/2008	207.28 -	03/2012 -	03/2021
	<u>Neyveli Lignite Corporation</u>				
5	TALABIRA II AND III OCP - [N06000189]NLC, ODISHA	07/2017	2,401.07 -	07/2020 -	04/2020
6	NEYVELI NEW THERMAL POWER PROJECT (2X500 MW) - [N06000095]NLC, TAMIL NADU	06/2011	5,907.11 7,980.79	12/2015 -	02/2021
7	HADLA LIGNITE MINE PROJECT (1.90 MTPA) - [N06000144]NLC, RAJASTHAN	03/2015	522.45 -	09/2019 -	-
8	BARSINGAR THERMAL POWER STATION EXTENSION - [N06000187]NLC, RAJASTHAN	03/2015	2,112.60 -	09/2020 -	-
9	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188]NLC, RAJASTHAN	03/2015	2,196.30 -	09/2020 -	-
10	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC, RAJASTHAN	03/2015	513.63 -	12/2019 -	-
	<u>Singareni Colliers Company Limited</u>				
11	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL, TELANGANA	11/2012	430.45 -	03/2016 -	03/2021
	<u>South-Eastern Coal Fields Limited</u>				
12	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH	12/2009	321.50 -	03/2014 -	03/2021
	<u>Western Coal Fields Limited</u>				
13	AMALGAMATED PAUNI-II III OC MINE - [N06000131]WCL, MAHARASHTRA	06/2015	483.69 499.00	03/2021 -	03/2021
	Total		18,583.15 -		
	<u>MINES</u>				
	<u>National Aluminum Company Limited (Nalco)</u>				
14	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]NALCO, TAMIL NADU	09/2017	166.62 163.17	06/2019 06/2021	12/2020

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
15	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]NALCO,ODISHA	12/2015	355.00 -	11/2020 -	02/2021
16	UTKAL D AND E COAL BLOCK - [N10000011]NALCO,ODISHA	05/2016	534.00 -	01/2020 -	-
	Total		1,055.62 -		
	<u>PETROLEUM</u>				
	<u>Bharat Petroleum Corporation Limited</u>				
17	PUNE POL STORAGE DEPOT - [N16000313]BPCL,MAHARASHTRA	08/2016	282.64 -	08/2020 -	03/2021
	<u>Chennai Petroleum Corporation Limited</u>				
18	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU	09/2017	1,858.00 -	12/2019 -	-
	<u>Hindustan Petroleum Corporation Limited</u>				
19	220 KV GRID SUPPLY - [N16000407]HPCL,ANDHRA PRADESH	10/2020	303.40 -	03/2021 -	-
20	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL,MAHARASHTRA	09/2015	4,199.00 5,060.00	03/2020 -	-
	<u>Indian Oil Corporation Limited</u>				
21	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]IOCL,ANDHRA PRADESH	08/2017	384.58 -	04/2021 03/2021	03/2021
22	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	06/2020 -	-
	<u>Oil India Limited</u>				
23	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	03/2017 -	03/2021
	Total		8,091.18 -		
	<u>POWER</u>				
	<u>National Hydro-Electric Power Corporation</u>				
24	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR	12/1999	578.62 -	06/2006 -	-
	<u>National Thermal Power Corporation</u>				
25	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	02/2017 -	01/2021
26	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000273]NTPC,UTTAR PRADESH	12/2018	587.44 -	09/2020 -	01/2021
27	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	03/2013	11,638.55 -	01/2018 -	02/2021
28	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH	09/2014	9,188.98 -	07/2019 03/2021	03/2021
29	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	09/2016 -	-
30	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	12/2012	11,846.00 -	10/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (April 2021)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
31	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	08/2017 -	-
32	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC,MADHYA PRADESH	03/2015	9,870.51 -	01/2020 -	-
33	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,238.00	10/2017 -	-
34	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH	09/2015	3,004.00 -	11/2019 -	-
35	JETSAR SOLAR 160 MW - [N18000287]NTPC,RAJASTHAN	12/2019	702.28 -	03/2021 -	-
	<u>North East Electric Power Corporation</u>				
36	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 7,927.34	12/2009 02/2021	-
	<u>Power Grid Corporation Of India Limited</u>				
37	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE	10/2016	408.46 516.12	01/2019 09/2020	04/2020
38	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE	09/2017	198.49 -	09/2019 09/2020	05/2020
39	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 1,891.41	04/2016 09/2020	07/2020
40	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT	05/2017	175.64 -	09/2018 11/2020	09/2020
41	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT	12/2017	193.14 -	06/2019 11/2020	09/2020
42	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE	01/2015	871.62 902.49	10/2017 05/2021	01/2021
43	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA	05/2017	445.89 675.73	02/2019 02/2021	02/2021
44	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 5,071.94	10/2012 11/2020	03/2021
45	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	06/2014 -	-
46	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	03/2018 -	-
47	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 -	07/2017 -	-
48	GREEN ENERGY CORRIDORS - INTER STATE TRANSSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE	05/2016	3,519.59 -	05/2019 -	-
49	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE	03/2017	283.72 -	11/2019 -	-
50	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE	10/2016	608.24 -	04/2019 -	-
51	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE	12/2015	3,654.00 -	04/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	Total		95,740.17		
	<u>HEAVY INDUSTRY</u>				
	<u>Bharat Heavy Electricals Limited</u>				
52	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHDL,DELHI	08/2016	1,554.00	09/2019	-
	Total		1,554.00		
	<u>HEALTH AND FAMILY WELFARE</u>				
	<u>Hospital Services Consultancy Corporation Ltd</u>				
53	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57	12/2014	03/2018
54	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL	08/2016	244.00	09/2018	05/2019
55	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL	12/2014	168.90	05/2017	07/2019
56	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA	09/2014	505.58	03/2018	09/2019
57	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65	05/2017	01/2020
58	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASHTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19	03/2019	01/2021
59	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA	01/2018	249.01	-	01/2021
60	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44	05/2017	03/2021
61	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95	02/2018	03/2021
62	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19	03/2019	03/2021
63	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH	03/2018	268.84	-	03/2021
	Total		2,809.32		
	<u>RAILWAYS</u>				
	<u>Central Railways</u>				
64	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06	03/2019	-
	<u>Container Corporation Of India</u>				
65	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH	01/2013	387.70	03/2018	03/2021
66	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00	03/2019	12/2020

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
67	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32 -	03/2019 -	03/2021
68	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	03/2018 -	-
69	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH	05/2014	207.00 -	03/2018 -	-
70	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	03/2019 -	-
71	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	03/2019 -	-
72	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	03/2019 -	-
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>				
73	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	11,589.00 30,357.00	- -	-
74	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE	11/2007	16,592.00 51,101.00	03/2020 -	-
	<u>East Central Railways</u>				
75	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR	04/1999	325.00 -	- -	03/2021
76	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	499.41 -	03/2020 -	-
77	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-
78	ARA-BHABHUA ROAD (NL) - [N22000166]ECR,BIHAR	04/2008	633.87 -	- -	-
79	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-
80	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR	04/2008	445.25 -	- -	-
81	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE	04/2008	415.67 -	- -	-
82	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-
83	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-
84	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-
85	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-
86	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
87	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-
88	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-
89	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR,BIHAR	04/1998	180.82 -	- -	-
	<u>Eastern Railways</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
90	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	05/2019
91	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	03/2021
92	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	11/2018 -	03/2021
93	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	542.18 -	03/2020 -	03/2021
	<u>Kolkata Metro Rail Corporation Limited</u>				
94	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-
	<u>Metropolitan Rapid Transport Projects</u>				
95	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-
96	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 -	03/2014 -	-
97	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	-
	<u>North Central Railway</u>				
98	ETAWAH-MAINPURI (NL), NCR - [220100318]NCR, UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-
99	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR, MULTI STATE	04/2010	2,030.50 -	- -	-
100	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR, UTTAR PRADESH	04/2015	668.70 668.00	03/2020 -	-
101	JHANSI BINA DOUBLING - [N22000496]NCR, UTTAR PRADESH	09/2016	2,001.00 -	03/2021 -	-
	<u>North East Frontier Railway</u>				
102	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR, ASSAM	04/2011	314.00 486.96	03/2019 -	03/2021
103	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR - [220100135]NFR, WEST BENGAL	04/1983	297.32 200.34	03/2019 -	-
104	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48 -	12/2015 -	-
105	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 -	- -	-
106	DIMAPUR-TIZIT NL - [N22000196]NFR, NAGALAND	04/2013	4,274.00 -	03/2020 -	-
107	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR, MEGHALAYA	04/2010	906.46 1,202.33	03/2021 -	-
108	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR, MULTI STATE	04/2010	242.22 -	03/2020 -	-
109	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR, MULTI STATE	04/1999	819.23 -	- -	-
110	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHOWA-JAIN - [N22000499]NFR, WEST BENGAL	02/1999	380.60 -	04/2010 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
111	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	333.76 -	- -	-
112	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	414.84 -	03/2020 -	-
	<u>North Eastern Railway</u>				
113	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH	04/2017	622.50 427.00	04/2017 -	03/2021
114	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-
115	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
116	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
117	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-
118	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-
	<u>North Western Railway</u>				
119	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	10/2018 -	01/2020
120	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	02/2019 -	02/2020
121	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	12/2019 -	02/2021
122	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	11/2019 -	03/2021
123	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-
124	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
125	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
126	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-
	<u>Northern Railway</u>				
127	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
	<u>Rail India Technical And Economic Service</u>				
128	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES,TELANGANA	03/2015	636.38 -	03/2021 -	03/2021
129	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-
	<u>Rail Vikas Nigam Ltd.</u>				
130	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT	04/2012	644.38 -	03/2021 -	03/2021
131	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	1,185.64 -	12/2017 -	-
132	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	03/2009 03/2009	-
	<u>Railway Electrification</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (April 2021)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
133	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-
	<u>South Central Railway</u>				
134	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	164.36 -	02/2009 -	-
135	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-
136	GUDUR-DURGARAJPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	761.37 -	- -	-
137	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
138	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-
	<u>South East Central Railway</u>				
139	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- -	-
140	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR,CHHATISGARH	04/2008	872.00 -	12/2019 -	-
	<u>South Eastern Railway</u>				
141	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	12/2016 -	08/2020
142	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-
143	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-
	<u>Southern Railway</u>				
144	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU	10/2013	187.26 -	04/2014 -	12/2020
145	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	1,566.00 -	- -	-
146	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	227.40 -	- -	-
147	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	151.84 -	02/2019 -	-
148	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
149	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
150	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
151	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-
152	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 -	- -	-
153	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	- -	-
154	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (April 2021)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
155	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU	02/1999	257.00 257.00	03/2018 -	-
	<u>Western Railway</u>				
156	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT	04/2017	691.84 1,017.91	03/2020 02/2021	02/2021
157	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-
158	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT	03/2017	243.60 -	- -	-
159	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-
160	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-
161	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-
162	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 -	- -	-
	Total		91,046.77 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
	<u>Central Public Works Department</u>				
163	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE - [N24001236]CPWD,TAMIL NADU	03/2019	297.55 -	11/2019 -	-
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>				
164	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]MoRTH,ANDHRA PRADESH	03/2018	504.19 504.00	11/2018 -	01/2021
165	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]MoRTH,ANDHRA PRADESH	03/2018	289.67 290.00	08/2018 -	02/2021
166	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]MoRTH,ANDHRA PRADESH	03/2015	271.45 -	10/2015 -	03/2021
167	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH	01/2012	410.72 -	04/2015 -	03/2021
168	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934]MoRTH,ANDHRA PRADESH	03/2018	228.32 -	08/2018 -	03/2021
169	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950]MoRTH,RAJASTHAN	11/2017	187.82 -	04/2018 -	03/2021
170	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709 - [N24000957]MoRTH,RAJASTHAN	11/2017	163.95 -	04/2018 -	03/2021
171	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MoRTH,RAJASTHAN	03/2019	178.13 -	- -	03/2021

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
172	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932]MoRTH,ANDHRA PRADESH	01/2017	319.28 -	08/2017 -	08/2019
173	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. - [N24001174]MoRTH,MANIPUR	10/2016	235.31 -	11/2020 -	11/2020
174	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]MoRTH,NAGALAND	03/2017	217.35 -	11/2020 05/2021	11/2020
175	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]MoRTH,MIZORAM	11/2010	624.41 -	03/2011 -	12/2020
176	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]MoRTH,PUNJAB	11/2015	889.24 -	- -	12/2020
177	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964]MoRTH,ANDHRA PRADESH	08/2016	350.61 -	01/2017 -	12/2020
178	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]MoRTH,NAGALAND	10/2016	167.62 -	12/2020 09/2021	12/2020
179	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]MoRTH,NAGALAND	10/2016	172.63 -	12/2020 09/2021	12/2020
180	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]MoRTH,WEST BENGAL	04/2014	279.70 398.52	08/2017 01/2020	02/2020
181	R AND U FROM KM 385.00 TO KM 420.000 TO 2- LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404 - [N24001205]MoRTH,UTTAR PRADESH	12/2016	209.10 -	10/2019 -	04/2020
182	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]MoRTH,CHHATISGARH	11/2015	485.44 -	12/2015 05/2020	05/2020
183	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH,ARUNACHAL PRADESH	11/2016	243.89 -	- -	09/2020
184	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 127.500 TO 178.944 DARRIGHAT TO BANARI SECTION - [N24001220]MoRTH,CHHATISGARH	03/2016	491.52 512.77	09/2016 10/2020	10/2020
185	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884]MoRTH,MADHYA PRADESH	03/2018	191.21 -	11/2019 -	01/2021
186	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131]MoRTH,JHARKHAND	03/2018	212.99 -	06/2020 -	01/2021
187	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH - [N24001145]MoRTH,UTTAR PRADESH	05/2013	164.54 165.00	08/2015 -	01/2021
188	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]MoRTH,UTTAR PRADESH	03/2018	185.18 -	02/2020 -	01/2021
189	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]MoRTH,MADHYA PRADESH	11/2017	235.91 -	02/2018 02/2021	02/2021

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
190	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]MoRTH,HARYANA	01/2017	247.25 -	03/2019 -	02/2021
191	REHABILITATION AND UPGRADATION OF HARPALPUR -SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942]MoRTH,UTTAR PRADESH	03/2016	208.50 -	11/2019 -	02/2021
192	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883]MoRTH,WEST BENGAL	03/2018	254.30 254.30	10/2020 -	03/2021
193	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH,UTTAR PRADESH	03/2016	240.30 240.00	01/2020 -	03/2021
194	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]MoRTH,UTTAR PRADESH	03/2016	249.50 -	05/2019 -	03/2021
195	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203]MoRTH,UTTAR PRADESH	10/2016	218.90 -	03/2020 -	03/2021
196	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]MoRTH,UTTAR PRADESH	07/2016	208.88 -	10/2019 -	03/2021
197	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONALI - GORAKHPUR ROAD (J - [N24001208]MoRTH,UTTAR PRADESH	03/2018	288.30 -	08/2020 -	03/2021
198	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO - [N24001224]MoRTH,CHHATISGARH	03/2017	423.79 -	01/2018 03/2021	03/2021
199	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]MoRTH,TELANGANA	01/2014	270.00 -	03/2016 -	-
200	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA	03/2015	153.21 -	01/2017 -	-
201	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]MoRTH,GOA	03/2015	297.00 -	04/2018 -	-
202	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]MoRTH,MAHARASHTRA	03/2015	168.30 -	- -	-
203	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]MoRTH,MAHARASHTRA	08/2014	187.79 -	07/2016 -	-
204	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]MoRTH,MAHARASHTRA	01/2014	446.77 -	- -	-
205	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]MoRTH,GOA	03/2015	298.33 -	- -	-
206	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]MoRTH,GOA	03/2015	184.05 -	- -	-
207	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]MoRTH,GOA	03/2015	280.16 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
208	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]MoRTH,KERALA	01/2014	255.75 348.00	09/2017 -	-
209	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]MoRTH,ANDHRA PRADESH	07/2015	333.21 333.21	12/2015 -	-
210	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MoRTH,MAHARASHTRA	10/2015	289.60 -	- -	-
211	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MoRTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-
212	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]MoRTH,ANDHRA PRADESH	01/2014	195.45 -	11/2014 -	-
213	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MoRTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-
214	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MoRTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-
215	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MoRTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-
216	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MoRTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-
217	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MoRTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-
218	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]MoRTH,ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	-
219	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]MoRTH,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-
220	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]MoRTH,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-
221	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]MoRTH,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 06/2018	-
222	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]MoRTH,NAGALAND	12/2010	1,296.00 -	02/2011 -	-
223	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MoRTH,TAMIL NADU	03/2015	258.97 -	08/2015 -	-
224	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MoRTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-
225	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I- - [N24000318]MoRTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
226	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MoRTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-
227	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA	01/2015	225.81 -	- -	-
228	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MoRTH,RAJASTHAN	12/2015	621.43 -	06/2018 -	-
229	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-
230	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MoRTH,KARNATAKA	03/2015	159.12 -	11/2015 -	-
231	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]MoRTH,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	-
232	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]MoRTH,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	-
233	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]MoRTH,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	-
234	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MoRTH,KARNATAKA	01/1991	219.40 -	01/2018 -	-
235	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MoRTH,ODISHA	01/1991	218.63 -	10/2017 -	-
236	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH,BIHAR	01/1991	675.00 -	- -	-
237	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]MoRTH,PUNJAB	12/2015	766.36 -	- -	-
238	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]MoRTH,PUNJAB	11/2015	847.02 -	- -	-
239	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]MoRTH,ASSAM	11/2010	268.08 -	05/2017 -	-
240	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]MoRTH,MADHYA PRADESH	08/2015	257.80 -	- -	-
241	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]MoRTH,ASSAM	11/2010	470.20 -	02/2011 -	-
242	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MoRTH,WEST BENGAL	01/1991	322.00 -	03/2018 -	-
243	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MoRTH,BIHAR	01/1991	282.41 -	08/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
244	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MoRTH, BIHAR	01/1991	358.22 -	10/2016 -	-
245	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]MoRTH, ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-
246	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MoRTH, ODISHA	01/1991	229.41 -	05/2018 -	-
247	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]MoRTH, ODISHA	07/2014	342.05 -	01/2017 -	-
248	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH, GOA	10/2015	936.40 -	- -	-
249	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]MoRTH, RAJASTHAN	09/2012	511.00 -	10/2013 -	-
250	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]MoRTH, RAJASTHAN	09/2012	511.00 -	10/2013 -	-
251	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH, UTTAR PRADESH	05/2013	164.54 -	08/2015 -	-
252	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH, GOA	12/2015	773.98 -	- -	-
253	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MoRTH, GOA	12/2015	819.95 -	- -	-
254	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MoRTH, BIHAR	01/1991	478.35 -	- -	-
255	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]MoRTH, ODISHA	12/2011	159.39 -	11/2017 -	-
256	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]MoRTH, PUNJAB	06/2015	892.17 -	- -	-
257	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH, ODISHA	12/2011	191.08 -	08/2015 -	-
258	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]MoRTH, BIHAR	01/1991	154.62 -	- -	-
259	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]MoRTH, BIHAR	01/1991	319.68 -	- -	-
260	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MoRTH, BIHAR	10/2013	278.39 -	08/2014 -	-
261	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MoRTH, BIHAR	11/2013	683.83 -	07/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (April 2021)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
262	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MoRTH,BIHAR	02/2014	665.50 -	07/2016 -	-
263	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MoRTH,BIHAR	02/2016	178.85 -	05/2016 -	-
264	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MoRTH,BIHAR	02/2016	369.77 -	06/2016 -	-
265	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MoRTH,BIHAR	02/2016	553.30 -	05/2016 -	-
266	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-
267	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPR - [N24000580]MoRTH,BIHAR	03/2015	206.80 -	07/2016 -	-
268	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MoRTH,BIHAR	08/2015	288.24 -	11/2015 -	-
269	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH,MAHARASHTRA	03/2016	1,142.62 -	- -	-
270	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH,MAHARASHTRA	03/2016	1,101.58 -	- -	-
271	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH,BIHAR	08/2016	1,742.01 -	12/2016 -	-
272	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH,ODISHA	03/2014	191.50 192.00	05/2016 -	-
273	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MoRTH,ODISHA	01/2015	326.63 327.00	04/2018 -	-
274	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MoRTH,ODISHA	02/2015	239.91 240.00	10/2017 -	-
275	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MoRTH,ODISHA	07/2014	342.05 342.00	01/2017 -	-
276	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH,ODISHA	08/2013	171.96 172.00	06/2016 -	-
277	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MoRTH,ODISHA	06/2016	157.30 157.00	06/2018 -	-
278	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH,UTTARAKHAND	12/2017	257.34 -	12/2019 -	-
279	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH,UTTARAKHAND	12/2017	200.34 -	12/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
280	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MoRTH,UTTARAKHAND	12/2017	248.22 -	12/2019 -	-
281	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MoRTH,UTTARAKHAND	06/2017	282.08 -	06/2019 -	-
282	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH,UTTARAKHAND	11/2017	232.81 -	11/2019 -	-
283	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH,UTTARAKHAND	11/2017	283.51 -	11/2019 -	-
284	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH,UTTARAKHAND	11/2017	266.52 -	11/2019 -	-
285	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MoRTH,UTTARAKHAND	02/2018	418.88 -	02/2020 -	-
286	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MoRTH,UTTARAKHAND	02/2018	293.68 -	- -	-
287	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MoRTH,UTTARAKHAND	05/2018	248.00 -	05/2020 -	-
288	REHABILITATION AND UPGADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH,UTTARAKHAND	03/2018	460.73 -	- -	-
289	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MoRTH,A & N ISLANDS	11/2017	237.80 -	11/2019 -	-
290	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH,A & N ISLANDS	11/2017	257.34 -	11/2019 -	-
291	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O - [N24000871]MoRTH,WEST BENGAL	08/2014	600.87 720.97	11/2017 -	-
292	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH	03/2018	166.21 -	08/2018 -	-
293	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873]MoRTH,WEST BENGAL	08/2014	823.20 937.76	11/2017 -	-
294	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879]MoRTH,WEST BENGAL	03/2017	202.69 202.69	11/2019 -	-
295	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906]MoRTH,PUNJAB	03/2018	173.24 -	06/2020 -	-
296	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]MoRTH,PUNJAB	03/2018	293.10 -	08/2020 -	-
297	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) - [N24000908]MoRTH,HARYANA	01/2017	276.01 -	03/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
298	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26. - [N24000911]MoRTH,ODISHA	03/2016	165.06 -	12/2016 -	-
299	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MoRTH,ODISHA	08/2016	287.70 -	02/2017 -	-
300	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH,ODISHA	09/2016	295.67 -	02/2017 -	-
301	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH,ODISHA	12/2016	223.50 -	08/2018 -	-
302	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH,ODISHA	12/2016	206.88 -	04/2018 -	-
303	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH,ODISHA	03/2018	214.23 -	08/2018 -	-
304	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH,ODISHA	03/2018	199.16 -	08/2018 -	-
305	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922]MoRTH,GUJARAT	12/2017	867.97 -	11/2018 -	-
306	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEEN - [N24000923]MoRTH,GUJARAT	03/2018	464.07 -	11/2018 -	-
307	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPIR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]MoRTH,GUJARAT	10/2018	400.76 -	05/2019 -	-
308	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926]MoRTH,GUJARAT	08/2017	962.43 -	03/2018 -	-
309	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927]MoRTH,PUNJAB	03/2018	293.64 -	08/2020 -	-
310	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]MoRTH,ANDHRA PRADESH	10/2015	333.21 -	12/2015 -	-
311	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO - [N24000930]MoRTH,ANDHRA PRADESH	11/2016	378.24 -	01/2018 -	-
312	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU - [N24000936]MoRTH,ANDHRA PRADESH	03/2018	244.95 245.00	08/2018 -	-
313	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938]MoRTH,ANDHRA PRADESH	03/2018	297.12 294.00	07/2018 -	-
314	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]MoRTH,PUNJAB	03/2018	293.64 -	08/2020 -	-
315	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR	09/2018	1,478.40 -	- -	-
316	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 - [N24000962]MoRTH,MADHYA PRADESH	09/2016	178.23 -	09/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
317	REHABILITATION AND UPGADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]MoRTH,ANDHRA PRADESH	01/2016	386.09 -	05/2016 -	-
318	REHABILITATION AND UPGADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967]MoRTH,ANDHRA PRADESH	03/2016	444.84 -	09/2016 -	-
319	REHABILITATION AND UPGADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]MoRTH,ANDHRA PRADESH	11/2016	376.25 -	08/2017 -	-
320	REHABILITATION AND UPGADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]MoRTH,ANDHRA PRADESH	01/2017	576.48 -	01/2018 -	-
321	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA	10/2016	298.32 -	02/2019 -	-
322	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA	10/2016	248.83 -	03/2019 -	-
323	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH,TELANGANA	01/2017	244.54 -	05/2019 -	-
324	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]MoRTH,TELANGANA	01/2017	196.52 -	10/2019 -	-
325	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]MoRTH,TELANGANA	01/2017	283.00 -	12/2019 -	-
326	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]MoRTH,TELANGANA	01/2017	359.27 -	05/2019 -	-
327	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH,TELANGANA	01/2017	300.00 -	05/2019 -	-
328	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]MoRTH,TELANGANA	01/2018	283.15 -	05/2020 -	-
329	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]MoRTH,TELANGANA	01/2018	230.03 -	12/2019 -	-
330	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]MoRTH,TELANGANA	02/2018	206.13 -	06/2020 -	-
331	REHABILITATION AND UPGADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH,TELANGANA	02/2018	294.13 -	11/2019 -	-
332	REHABILITATION AND UPGADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH,TELANGANA	02/2018	220.28 -	11/2019 -	-
333	REHABILITATION AND UPGADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]MoRTH,TELANGANA	02/2018	426.52 -	04/2020 -	-
334	REHABILITATION AND UPGADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]MoRTH,TELANGANA	03/2018	322.81 -	09/2020 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
335	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]MoRTH,TELANGANA	03/2018	626.76 -	07/2020 -	-
336	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH,TELANGANA	01/2017	605.08 -	10/2019 -	-
337	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH,TELANGANA	03/2018	192.67 -	07/2019 -	-
338	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH,TELANGANA	01/2019	193.19 -	- -	-
339	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C - [N24000999]MoRTH,BIHAR	11/2016	230.34 -	10/2019 -	-
340	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH,BIHAR	03/2018	153.24 -	- -	-
341	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]MoRTH,BIHAR	05/2014	199.98 -	08/2016 -	-
342	SARSAM TO KOTHARI - [N24001002]MoRTH,MAHARASHTRA	02/2016	545.64 -	07/2019 -	-
343	AKOLA TO AKOT - [N24001003]MoRTH,MAHARASHTRA	01/2017	313.95 -	06/2019 -	-
344	PATRADEVI TO KARASWADA 4L - [N24001004]MoRTH,GOA	03/2017	634.32 -	05/2020 -	-
345	KARASWADA TO BAMBOLIM - [N24001005]MoRTH,GOA	03/2017	852.67 -	12/2019 -	-
346	AKOT TO ANJANGAON - [N24001006]MoRTH,MAHARASHTRA	01/2017	245.77 246.00	06/2019 -	-
347	ANJANGAON TO MAH/MP BORDER - [N24001007]MoRTH,MADHYA PRADESH	01/2017	359.00 359.00	06/2019 -	-
348	AJANTHA TO BULDHANA - [N24001008]MoRTH,A & N ISLANDS	02/2017	401.00 401.00	07/2019 -	-
349	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA	02/2017	203.21 203.00	05/2019 -	-
350	SHEGAON TO DEORI PHATA - [N24001010]MoRTH,MAHARASHTRA	02/2017	373.10 373.00	05/2019 -	-
351	MEHKAR TO CHIKALI - [N24001011]MoRTH,MAHARASHTRA	02/2017	322.48 322.00	05/2019 -	-
352	CHIKALI TO KHAMGAON - [N24001012]MoRTH,MAHARASHTRA	02/2017	548.03 548.00	06/2019 -	-
353	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA	01/2017	391.06 391.00	06/2019 -	-
354	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA	01/2017	385.87 386.00	06/2019 -	-
355	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA	01/2017	341.16 341.00	06/2019 -	-
356	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH,MAHARASHTRA	01/2017	471.61 472.00	06/2019 -	-
357	DAHEGAON TO KUIH - [N24001017]MoRTH,MAHARASHTRA	01/2017	228.89 229.00	06/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
358	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA	01/2017	392.83 393.00	06/2019 -	-
359	KATOL TO WARUD - [N24001019]MoRTH,MAHARASHTRA	01/2017	463.62 664.00	06/2019 -	-
360	AMDIT TO SAONER - [N24001021]MoRTH,MAHARASHTRA	01/2017	396.91 397.00	06/2019 -	-
361	WADI TO ASOLA - [N24001022]MoRTH,MAHARASHTRA	01/2017	363.82 364.00	09/2019 -	-
362	NAGAJ TO VAJAPUR - [N24001023]MoRTH,MAHARASHTRA	01/2017	376.72 377.00	06/2019 -	-
363	MANGAON TO DIGHI PORT - [N24001024]MoRTH,MAHARASHTRA	01/2017	457.52 -	07/2019 -	-
364	INDAPUR TO AGARDANDA - [N24001025]MoRTH,MAHARASHTRA	01/2017	355.17 -	07/2019 -	-
365	WAKAN PALI KHOPOLI - [N24001026]MoRTH,MAHARASHTRA	01/2017	376.19 -	05/2019 -	-
366	SHAHPUR PATGAON SECTION I - [N24001027]MoRTH,MAHARASHTRA	01/2018	150.79 -	12/2019 -	-
367	PATGAON KHOPOLI SECTION I - [N24001028]MoRTH,MAHARASHTRA	01/2018	170.00 -	12/2019 -	-
368	AHMADPUR TO PIMPLA - [N24001029]MoRTH,MAHARASHTRA	01/2017	422.38 -	08/2019 -	-
369	PIMPLA TO MANJARSUMBHA - [N24001030]MoRTH,MAHARASHTRA	01/2017	595.77 -	08/2019 -	-
370	MANJUSUMBA TO CHUMBALI - [N24001031]MoRTH,MAHARASHTRA	01/2017	228.54 -	08/2019 -	-
371	DEORI TO AMGAON - [N24001032]MoRTH,MAHARASHTRA	01/2017	409.62 410.00	05/2019 -	-
372	MANTHA TALUKAS BORDER TO PARTUR - [N24001033]MoRTH,MAHARASHTRA	01/2017	486.19 -	07/2019 -	-
373	PARTUR TO MAJALGAON - [N24001034]MoRTH,MAHARASHTRA	01/2017	420.57 -	07/2019 -	-
374	MANSAR TO SALAIKHURD - [N24001035]MoRTH,MAHARASHTRA	01/2018	418.36 -	12/2019 -	-
375	MAJALGAON TO KAIJ - [N24001036]MoRTH,MAHARASHTRA	01/2017	413.99 -	07/2019 -	-
376	KAIJ TO KUSALAM - [N24001037]MoRTH,MAHARASHTRA	01/2017	554.78 -	07/2019 -	-
377	MAHAD TO RAIGAD FORT - [N24001038]MoRTH,MAHARASHTRA	07/2018	237.40 -	05/2020 -	-
378	JINTUR TO PARBHANI - [N24001039]MoRTH,MAHARASHTRA	01/2017	356.66 -	- -	-
379	JAHIRABAD TO LATUR - [N24001040]MoRTH,MAHARASHTRA	01/2017	461.96 -	11/2019 -	-
380	SHIROD SHAHPURER TO NANDED - [N24001041]MoRTH,MAHARASHTRA	01/2017	211.34 -	07/2019 -	-
381	SALAIKHURD TO TIRORA - [N24001042]MoRTH,MAHARASHTRA	01/2018	415.25 415.25	12/2019 -	-
382	NILAJPHATA TO BHANDARA - [N24001043]MoRTH,MAHARASHTRA	01/2018	420.63 421.00	05/2020 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
383	KALMAB TO RALEGAON - [N24001044]MoRTH,MAHARASHTRA	01/2017	467.78 -	06/2019 -	-
384	JALGAON TO BHADGAON - [N24001045]MoRTH,MAHARASHTRA	01/2018	307.54 308.00	11/2019 -	-
385	RALEGAON TO RAMTIRTH - [N24001046]MoRTH,MAHARASHTRA	01/2017	210.81 -	07/2019 -	-
386	BHADGAON TO CHALISGAON - [N24001047]MoRTH,MAHARASHTRA	01/2018	259.55 260.00	11/2019 -	-
387	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA	01/2017	232.77 -	07/2019 -	-
388	KARAD TO VITA - [N24001049]MoRTH,MAHARASHTRA	01/2018	344.85 245.00	12/2019 -	-
389	VITA TO NAGAJ - [N24001050]MoRTH,MAHARASHTRA	03/2018	304.58 305.00	12/2019 -	-
390	NALDURG TO AKKALKOT - [N24001051]MoRTH,MAHARASHTRA	02/2018	274.50 275.00	12/2019 -	-
391	SANGOLA TO JATH - [N24001052]MoRTH,MAHARASHTRA	01/2018	257.38 257.00	12/2019 -	-
392	KARAD TO TAGAON - [N24001053]MoRTH,MAHARASHTRA	01/2017	537.81 538.00	06/2019 -	-
393	TASGAON TO SHIRDHON - [N24001054]MoRTH,MAHARASHTRA	01/2017	195.64 196.00	11/2019 -	-
394	HELWAK TO KARAD - [N24001055]MoRTH,MAHARASHTRA	02/2017	416.99 -	07/2019 -	-
395	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA	02/2017	422.02 422.00	07/2019 -	-
396	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MoRTH,MAHARASHTRA	02/2017	407.19 407.00	06/2019 -	-
397	KARWANDI TO RAJURI - [N24001058]MoRTH,MAHARASHTRA	03/2018	276.95 277.00	12/2019 -	-
398	SHIVUR TO YEOLA - [N24001059]MoRTH,MAHARASHTRA	03/2018	181.08 -	12/2019 -	-
399	PALPHATA TO PHULAMBARI - [N24001060]MoRTH,MAHARASHTRA	03/2018	227.19 227.00	12/2019 -	-
400	CHIKALI TO DHAD - [N24001061]MoRTH,MAHARASHTRA	03/2018	189.46 189.00	12/2019 -	-
401	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]MoRTH,MAHARASHTRA	03/2018	336.21 336.00	12/2019 -	-
402	WADIGODRI TO DHANGRIIMPRI - [N24001063]MoRTH,MAHARASHTRA	03/2018	194.23 194.00	02/2020 -	-
403	DHANGRIIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]MoRTH,MAHARASHTRA	03/2018	217.14 217.00	02/2020 -	-
404	PARBHANI TO GANGKHED - [N24001065]MoRTH,MAHARASHTRA	03/2018	238.19 238.00	12/2019 -	-
405	LATUR TO PANGAON - [N24001066]MoRTH,MAHARASHTRA	03/2018	336.47 336.00	12/2019 -	-
406	OMREGA TO AUSA - [N24001067]MoRTH,MAHARASHTRA	03/2018	272.04 272.00	12/2019 -	-
407	WASHIM TO DASTAPUR - [N24001068]MoRTH,MAHARASHTRA	03/2018	165.51 -	12/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
408	NANDED TO JALKOT - [N24001069]MoRTH,MAHARASHTRA	12/2017	456.93 457.00	09/2019 -	-
409	DASTAPUR TO KARANJA - [N24001070]MoRTH,MAHARASHTRA	03/2018	182.63 -	12/2019 -	-
410	JALKOT TO TOGRI - [N24001071]MoRTH,MAHARASHTRA	07/2018	299.92 300.00	08/2020 -	-
411	KHERDA TO NAGZARI - [N24001072]MoRTH,MAHARASHTRA	03/2018	181.30 -	12/2019 -	-
412	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA	09/2018	301.38 301.00	08/2020 -	-
413	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA	03/2018	249.29 -	12/2019 -	-
414	OSMANNAGAR TO KUNDAL - [N24001075]MoRTH,MAHARASHTRA	09/2017	344.25 344.00	08/2020 -	-
415	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA	03/2018	219.91 -	12/2019 -	-
416	KUNDAL TO WAZAR - [N24001077]MoRTH,MAHARASHTRA	01/2018	225.25 225.00	12/2019 -	-
417	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA	03/2018	228.31 -	12/2019 -	-
418	ARDHAPUR TO HIMAYATNAGAR - [N24001079]MoRTH,MAHARASHTRA	12/2017	426.06 426.00	06/2020 -	-
419	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA	03/2018	256.15 -	12/2019 -	-
420	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]MoRTH,MAHARASHTRA	03/2018	294.87 295.00	12/2019 -	-
421	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA	03/2018	223.46 -	12/2019 -	-
422	CHIKLI TO TAKARKHED - [N24001083]MoRTH,MAHARASHTRA	03/2018	393.10 393.00	12/2019 -	-
423	PAHUR TO BODHWAD - [N24001084]MoRTH,MAHARASHTRA	01/2017	244.93 -	05/2020 -	-
424	TAKARKHED TO JALNA - [N24001085]MoRTH,MAHARASHTRA	09/2017	417.90 418.00	06/2019 -	-
425	BODHWAD TO STATE BORDER - [N24001086]MoRTH,MAHARASHTRA	01/2017	178.26 -	07/2019 -	-
426	MANGRUPHIR TO MAHAN - [N24001087]MoRTH,MAHARASHTRA	03/2018	222.13 222.00	11/2019 -	-
427	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA	03/2018	177.84 177.00	12/2019 -	-
428	MALEGAON TO RISOD - [N24001089]MoRTH,MAHARASHTRA	02/2018	303.24 303.00	12/2019 -	-
429	KOLDE TO KHETIYA - [N24001090]MoRTH,MAHARASHTRA	01/2017	509.18 -	07/2019 -	-
430	SATARA TO MHASWAD - [N24001092]MoRTH,MAHARASHTRA	01/2017	653.46 -	07/2019 -	-
431	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA	12/2017	309.94 310.00	12/2019 -	-
432	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA	12/2017	244.04 244.00	03/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
433	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA	01/2017	388.44 -	- -	-
434	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA	01/2018	264.41 264.00	03/2019 -	-
435	SELDOH TO PANVAR - [N24001097]MoRTH,MAHARASHTRA	07/2018	404.33 404.00	05/2020 -	-
436	WARDHA TO HINGAGHAT - [N24001098]MoRTH,MAHARASHTRA	01/2018	216.90 217.00	12/2019 -	-
437	MHASWAD TO TEMBHURNI - [N24001099]MoRTH,MAHARASHTRA	01/2017	488.60 -	07/2019 -	-
438	AHMEDNAGAR TO BARAMATI - [N24001100]MoRTH,MAHARASHTRA	01/2017	955.40 -	08/2019 -	-
439	KURUDWADI TO PANDHARPUR - [N24001101]MoRTH,MAHARASHTRA	01/2017	307.63 -	07/2019 -	-
440	PANDHARPUR TO SANGOLA - [N24001102]MoRTH,MAHARASHTRA	07/2017	218.38 -	07/2019 -	-
441	SARAD VANI PIMPALGAON - [N24001103]MoRTH,MAHARASHTRA	01/2017	250.46 -	07/2019 -	-
442	MALEWADA TO CHIMUR - [N24001104]MoRTH,MAHARASHTRA	10/2016	322.55 -	06/2019 -	-
443	CHIMUR TO WARORA - [N24001105]MoRTH,MAHARASHTRA	11/2016	467.70 -	03/2019 -	-
444	PEN TO KHOPOLI - [N24001106]MoRTH,MAHARASHTRA	03/2018	301.39 302.00	03/2018 -	-
445	PANCHARAL TO MANDANGHAR - [N24001107]MoRTH,MAHARASHTRA	07/2018	381.08 302.00	05/2020 -	-
446	CHALISGAON TO NANDGAON - [N24001108]MoRTH,MAHARASHTRA	03/2018	206.97 207.00	12/2019 -	-
447	KUSUMBA TO MALEGAON - [N24001109]MoRTH,MAHARASHTRA	03/2018	243.45 244.00	12/2019 -	-
448	BAMNI TO NAVAEGAON - [N24001110]MoRTH,MAHARASHTRA	09/2017	241.69 242.00	04/2020 -	-
449	KOLHA TO NASRATPUR - [N24001111]MoRTH,MAHARASHTRA	04/2016	281.78 282.00	04/2019 -	-
450	NASRATPUR TO BARASGAON - [N24001112]MoRTH,MAHARASHTRA	07/2016	406.54 407.00	09/2019 -	-
451	INDAPUR TO VADPALE - [N24001114]MoRTH,MAHARASHTRA	01/2017	1,202.52 1,203.00	12/2019 -	-
452	VADPALE TO BHOGAN KHURD - [N24001115]MoRTH,MAHARASHTRA	01/2017	1,598.47 1,560.00	11/2019 -	-
453	GADCHIROLI TO MUL - [N24001116]MoRTH,MAHARASHTRA	12/2016	484.15 -	06/2019 -	-
454	MUL TO CHANDRAPUR - [N24001117]MoRTH,MAHARASHTRA	12/2016	162.34 -	07/2019 -	-
455	SAKOLI TO BHANDARA - [N24001118]MoRTH,MAHARASHTRA	01/2017	362.96 -	06/2019 -	-
456	NAGBHID TO ARMORI - [N24001119]MoRTH,MAHARASHTRA	09/2016	269.05 -	07/2019 -	-
457	AKKALKOT TO DHUDHNI - [N24001120]MoRTH,MAHARASHTRA	04/2016	211.42 -	02/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
458	NASHIK TO PETH - [N24001121]MoRTH,MAHARASHTRA	12/2015	289.60 -	11/2018 -	-
459	PAITHAN TO SHIRUR - [N24001122]MoRTH,MAHARASHTRA	03/2017	341.80 -	06/2019 -	-
460	SHIRUR TO KHARDA - [N24001123]MoRTH,MAHARASHTRA	02/2017	381.77 -	06/2019 -	-
461	AURANGABAD TO SILLOD - [N24001124]MoRTH,MAHARASHTRA	02/2017	456.32 -	06/2019 -	-
462	SILLOD TO FARDAPUR - [N24001125]MoRTH,MAHARASHTRA	02/2017	337.46 -	06/2019 -	-
463	FARDAPUR TO JALGAON - [N24001126]MoRTH,MAHARASHTRA	02/2017	456.45 -	06/2019 -	-
464	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA	02/2017	406.51 -	06/2019 -	-
465	BHOKAR TO SARSAM - [N24001128]MoRTH,MAHARASHTRA	02/2017	295.09 -	07/2019 -	-
466	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND	08/2016	234.88 -	12/2017 -	-
467	PARSHURAM GHAT TO ARAWALI - [N24001133]MoRTH,MAHARASHTRA	04/2016	983.14 983.00	12/2019 -	-
468	KANTE TO WAKED - [N24001134]MoRTH,MAHARASHTRA	03/2016	1,230.02 1,230.00	11/2019 -	-
469	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	-
470	TALGAON TO KALMATH - [N24001136]MoRTH,MAHARASHTRA	10/2016	904.70 905.00	03/2020 -	-
471	KALMATH TO ZARAP - [N24001137]MoRTH,MAHARASHTRA	09/2016	1,338.13 1,338.00	03/2020 -	-
472	PARLI PIMPLA DAHIGUDA - [N24001138]MoRTH,MAHARASHTRA	02/2017	205.72 206.00	06/2019 -	-
473	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA - [N24001139]MoRTH,UTTAR PRADESH	10/2016	218.94 219.00	03/2020 -	-
474	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]MoRTH,UTTAR PRADESH	11/2016	215.16 215.00	09/2019 -	-
475	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO - [N24001143]MoRTH,UTTAR PRADESH	10/2016	176.94 177.00	10/2018 -	-
476	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2- - [N24001147]MoRTH,UTTAR PRADESH	10/2016	239.63 -	02/2019 -	-
477	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148]MoRTH,UTTAR PRADESH	03/2016	599.34 -	01/2020 -	-
478	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA	02/2018	355.99 -	12/2019 -	-
479	WARDHA TO ARVI - [N24001150]MoRTH,MAHARASHTRA	02/2018	313.58 -	04/2020 -	-
480	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM - [N24001153]MoRTH,ASSAM	11/2010	197.37 -	02/2014 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
481	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT - [N24001154]MoRTH,KARNATAKA	08/2016	367.44 -	01/2017 -	-
482	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT - [N24001155]MoRTH,KARNATAKA	08/2016	175.20 -	01/2017 -	-
483	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS - PA - [N24001156]MoRTH,KARNATAKA	01/2017	166.67 -	09/2017 -	-
484	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA	08/2016	175.50 -	02/2017 -	-
485	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA	03/2018	159.97 -	06/2019 -	-
486	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]MoRTH,KARNATAKA	01/2018	159.70 -	07/2018 -	-
487	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA	09/2017	191.60 -	10/2018 -	-
488	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]MoRTH,KARNATAKA	12/2017	297.30 -	01/2019 -	-
489	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA	03/2018	325.86 -	10/2018 -	-
490	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]MoRTH,KARNATAKA	08/2016	329.01 -	02/2017 -	-
491	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA	10/2016	396.96 -	03/2017 -	-
492	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA	11/2016	314.90 -	03/2017 -	-
493	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA	03/2015	159.12 -	01/2016 -	-
494	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776) - [N24001167]MoRTH,KARNATAKA	03/2015	165.67 -	01/2016 -	-
495	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA	05/2018	171.60 -	05/2018 -	-
496	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM. - [N24001170]MoRTH,KARNATAKA	01/2014	471.16 -	08/2014 -	-
497	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA	01/2017	291.49 -	08/2017 -	-
498	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND	11/2016	336.25 369.96	09/2019 11/2020	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
499	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S - [N24001183]MoRTH,ANDHRA PRADESH	07/2014	251.55 -	02/2015 -	-
500	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR	02/2019	2,926.42 -	- -	-
501	REHABILITATION AND UPGRADATION OF BARAICH -SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA - [N24001202]MoRTH,UTTAR PRADESH	03/2016	388.83 -	12/2019 -	-
502	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH,UTTAR PRADESH	03/2018	306.59 -	- -	-
503	IMPROVEMENT AND UP-GRADATION OF EXISITING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH,UTTAR PRADESH	11/2018	281.45 -	- -	-
504	WIDENING OF SL TO 2 L KM. 107-184.80 SUKUMA TO KONTA ON NH 221 - [N24001223]MoRTH,CHANDIGARH	03/2010	179.89 271.00	03/2013 05/2019	-
505	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1 - [N24001225]MoRTH,CHANDIGARH	12/2010	169.26 299.00	01/2019 -	-
506	WIDENING TO 4 LANE / 4 LANE WITH PAVED SHOULDERS WITH STRENGTHENING OF EXISTING CARRIAGEWAY IN KM 0/ - [N24001237]MoRTH,TAMIL NADU	01/2016	162.72 -	09/2016 -	-
507	CONSTRUCTION OF FLYOVER FROM KM 604/252 TO 607/060 (MARTHANDAM JUNCTION) AND FROM KM 630/116 TO 631/ - [N24001238]MoRTH,TAMIL NADU	05/2016	307.70 -	01/2017 -	-
508	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM - [N24001239]MoRTH,TAMIL NADU	03/2018	240.38 -	06/2019 -	-
509	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W - [N24001243]MoRTH,ASSAM	03/2020	166.94 -	12/2020 -	-
510	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1) - [N24001289]MoRTH,ARUNACHAL PRADESH	03/2019	403.68 -	02/2020 -	-
511	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2 - [N24001290]MoRTH,ARUNACHAL PRADESH	03/2019	342.55 -	02/2020 -	-
512	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE - [N24001291]MoRTH,ARUNACHAL PRADESH	03/2019	421.48 -	11/2020 -	-
513	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE - [N24001292]MoRTH,ARUNACHAL PRADESH	03/2019	543.05 -	11/2020 -	-
514	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE - [N24001293]MoRTH,ARUNACHAL PRADESH	03/2019	486.70 -	10/2020 -	-
515	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE - [N24001294]MoRTH,ARUNACHAL PRADESH	03/2019	560.39 -	02/2020 -	-
516	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE - [N24001295]MoRTH,ARUNACHAL PRADESH	03/2019	347.78 -	09/2020 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
517	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG - [N24001296]MoRTH,ARUNACHAL PRADESH	03/2019	394.27 -	10/2020 -	-
518	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE - [N24001297]MoRTH,ARUNACHAL PRADESH	03/2019	450.65 -	11/2020 -	-
519	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 - [N24000895]MoRTH,MADHYA PRADESH	09/2016	287.34 -	01/2019 09/2020	11/2020
520	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH,ARUNACHAL PRADESH	09/2011	1,979.00 -	- 03/2020	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>				
521	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL,ARUNACHAL PRADESH	10/2015	210.50 210.50	- 01/2016	01/2019
522	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND	02/2017	387.00 -	09/2018 -	09/2020
523	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM	05/2015	454.89 -	05/2018 -	12/2020
524	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 -	04/2017 -	02/2021
525	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH	03/2017	284.09 284.09	04/2017 03/2018	03/2021
526	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL,ASSAM	06/2016	829.00 -	01/2019 -	-
527	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM	03/2015	168.39 -	11/2018 -	-
528	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM	10/2014	588.95 -	11/2018 -	-
529	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH	07/2015	197.16 -	10/2018 -	-
530	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH	03/2015	394.00 -	06/2018 -	-
531	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA	10/2014	369.00 -	03/2018 -	-
532	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM	12/2015	223.30 -	06/2018 -	-
533	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-
534	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM	12/2015	289.99 -	12/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (April 2021)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
535	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM	01/2016	252.00 -	01/2016 -	-
536	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH	04/2016	245.79 -	- -	-
537	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH	04/2016	198.00 -	10/2016 -	-
538	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH	11/2015	434.06 -	- -	-
539	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH	12/2016	138.93 155.00	01/2017 -	-
540	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH	02/2017	195.23 -	04/2017 -	-
541	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH	02/2017	203.36 -	04/2017 -	-
542	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH	01/2017	194.66 -	04/2017 -	-
543	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH	02/2017	167.28 -	04/2017 -	-
544	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND	02/2017	507.68 -	04/2017 -	-
545	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH	01/2017	198.22 -	04/2017 -	-
546	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM	04/2017	388.00 -	10/2017 -	-
547	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND	03/2018	274.31 -	05/2018 -	-
548	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND	03/2018	403.36 -	06/2018 -	-
549	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND	03/2018	417.24 -	05/2018 -	-
550	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS	03/2015	262.97 -	10/2018 -	-
551	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS	03/2017	409.85 -	12/2017 -	-
552	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS	03/2015	277.17 -	04/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
553	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS	02/2018	391.00 -	10/2018 -	-
554	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS	03/2018	234.27 -	10/2018 -	-
555	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND	03/2018	237.72 -	09/2018 -	-
556	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND	03/2018	251.97 -	09/2018 -	-
557	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND	03/2018	282.98 -	09/2018 -	-
558	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA - [N24000766]NHIDCL,SIKKIM	04/2017	318.42 -	11/2017 -	-
559	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM	03/2017	375.80 -	- -	-
560	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM	11/2017	290.05 -	11/2017 -	-
561	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM	03/2018	264.84 -	06/2018 -	-
562	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM	03/2015	829.00 -	01/2016 -	-
563	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL,UTTARAKHAND	03/2018	1,383.78 -	07/2018 -	-
564	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866]NHIDCL,JAMMU AND KASHMIR	03/2018	404.17 -	08/2018 -	-
565	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM - [N24000867]NHIDCL,JAMMU AND KASHMIR	03/2018	216.00 -	11/2018 -	-
566	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR	03/2018	253.44 -	07/2019 -	-
567	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL,ASSAM	10/2017	818.00 -	- -	-
568	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA	03/2019	306.28 -	05/2019 -	-
569	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH	12/2016	200.44 -	- -	-
570	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH	03/2017	1,718.59 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
571	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH	09/2016	568.92 -	- -	-
572	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH	12/2016	188.78 -	- -	-
573	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN - [N24000978]NHIDCL,ARUNACHAL PRADESH	03/2015	172.75 -	- -	-
574	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI - [N24000979]NHIDCL,ARUNACHAL PRADESH	01/2017	256.66 -	- -	-
575	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8 - [N24001184]NHIDCL,DELHI	07/2017	269.69 -	09/2019 -	-
576	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL,ASSAM	03/2017	1,049.51 -	- -	-
<u>National Highways Authority Of India</u>					
577	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- -	01/2020
578	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	- -	01/2021
579	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN	09/2016	1,239.82 -	- -	01/2021
580	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	09/2017 -	01/2021
581	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	03/2019 -	02/2021
582	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	07/2016 -	02/2021
583	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 -	03/2021
584	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	03/2021
585	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	06/2018 -	03/2021
586	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	08/2019 -	03/2021
587	4-LANNING OF KODEBAD-DHMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	03/2019 -	03/2021
588	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	- -	08/2020
589	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	10/2017 -	11/2020
590	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	04/2018 -	12/2020

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
591	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	06/2015
592	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- 06/2015	06/2015
593	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	07/2018
594	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 -	06/2019
595	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	04/2010 -	07/2019
596	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 -	09/2019
597	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	06/2019 -	09/2019
598	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 627.93	01/2016 01/2020	01/2020
599	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 686.13	- -	05/2020
600	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 679.94	- -	05/2020
601	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	06/2020
602	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 -	08/2020
603	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	09/2020
604	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN	02/2018	1,103.88 -	- -	09/2020
605	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI-ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	10/2020
606	SRINAGAR TO BANIHAI - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	10/2020
607	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 -	- -	10/2020
608	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	05/2018 11/2020	11/2020
609	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	03/2019 -	11/2020
610	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 469.31	01/2014 12/2020	12/2020
611	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 417.68	01/2016 12/2020	12/2020
612	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	08/2016 -	12/2020
613	FOUR LANING OF RAMBAN - BANIHAI SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	12/2020

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (April 2021)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
614	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20 -	04/2020 -	12/2020
615	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA	03/2018	1,484.30 -	- 06/2021	12/2020
616	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 585.00	11/2013 12/2020	01/2021
617	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR	12/2017	1,471.75 1,339.00	- -	01/2021
618	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI, GUJARAT	02/2018	1,052.21 -	- -	01/2021
619	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	04/2008 -	02/2021
620	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	07/2018 -	02/2021
621	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI, GUJARAT	06/2017	1,958.88 -	06/2020 -	02/2021
622	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH	03/2018	565.09 -	- -	02/2021
623	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	03/2021
624	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	11/2018 07/2019	03/2021
625	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	08/2018 -	03/2021
626	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	- -	03/2021
627	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	- -	03/2021
628	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH	03/2018	1,029.96 -	- -	03/2021
629	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	-
630	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	-
631	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	-
632	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-
633	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	-
634	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
635	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	-
636	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	09/2012 -	-
637	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	08/2011 -	-
638	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	-
639	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	-
640	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	06/2018 -	-
641	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	-
642	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-
643	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-
644	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-
645	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-
646	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	-
647	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-
648	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	-
649	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-
650	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	-
651	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	-
652	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-
653	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	-
654	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	-
655	MUZZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	-
656	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	-
657	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	10/2013 -	-
658	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	06/2015 -	-
659	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
660	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI, GUJARAT	01/2013	2,125.24 -	12/2015 -	-
661	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI, MAHARASHTRA	05/2013	1,348.20 -	02/2014 -	-
662	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI, HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	-
663	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI, TELANGANA	04/2014	1,266.60 -	09/2016 -	-
664	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI, RAJASTHAN	09/2014	425.19 -	09/2016 -	-
665	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI, TAMIL NADU	05/2015	1,387.11 -	11/2017 -	-
666	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI, TAMIL NADU	06/2015	563.92 -	12/2017 -	-
667	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI, UTTAR PRADESH	05/2015	261.09 -	05/2017 -	-
668	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI, TAMIL NADU	07/2014	401.11 -	01/2017 -	-
669	VADODARA-SURAT SECTION - [N24000361]NHAI, GUJARAT	03/2014	503.16 -	08/2016 -	-
670	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI, UTTAR PRADESH	09/2015	368.73 -	09/2016 -	-
671	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI, RAJASTHAN	10/2015	597.00 -	10/2017 -	-
672	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI, MAHARASHTRA	07/2015	2,288.18 -	05/2019 -	-
673	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL	10/2015	361.15 -	- -	-
674	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI, MAHARASHTRA	07/2015	1,885.74 -	05/2019 -	-
675	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI, HARYANA	12/2015	602.95 -	06/2016 -	-
676	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI, RAJASTHAN	08/2014	822.90 -	04/2018 -	-
677	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI, HARYANA	01/2016	574.28 -	07/2018 -	-
678	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI, UTTAR PRADESH	07/2015	1,657.20 -	01/2019 -	-
679	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI, MAHARASHTRA	01/2015	972.50 -	07/2017 -	-
680	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI, MAHARASHTRA	06/2014	923.04 -	11/2016 -	-
681	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI, UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-
682	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL	12/2015	1,083.00 -	06/2018 -	-
683	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI, BIHAR	08/2015	556.07 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
684	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI, RAJASTHAN	02/2008	1,673.70 -	10/2011 -	-
685	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI, HIMACHAL PRADESH	09/2015	934.46 -	03/2018 -	-
686	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI, BIHAR	12/2015	1,041.10 -	04/2019 -	-
687	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI, JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	-
688	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI, KARNATAKA	03/2015	1,388.00 -	08/2018 -	-
689	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI, UTTAR PRADESH	01/2016	815.28 -	06/2018 -	-
690	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI, UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	-
691	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI, MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	-
692	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI, CHHATISGARH	12/2015	596.67 -	05/2018 -	-
693	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI, MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	-
694	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI, UTTAR PRADESH	06/2016	667.00 -	07/2018 -	-
695	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI, UTTAR PRADESH	12/2015	667.00 -	06/2018 -	-
696	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI, CHHATISGARH	12/2015	509.13 -	04/2018 -	-
697	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI, PUNJAB	10/2015	447.29 -	12/2017 -	-
698	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI, BIHAR	01/1991	642.41 -	- -	-
699	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI, BIHAR	12/2015	1,167.45 -	- -	-
700	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI, MAHARASHTRA	07/2015	1,871.34 -	01/2018 -	-
701	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI, MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	-
702	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL	04/2014	1,665.00 -	- -	-
703	TWO LANING WITH PS OF JOWAI - MEHALAYA / ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI, MEGHALAYA	12/2015	479.20 -	05/2018 -	-
704	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI, BIHAR	08/2015	399.54 -	04/2019 -	-
705	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS - DHOLPUR - [N24000520]NHAI, RAJASTHAN	08/2015	275.90 -	- -	-
706	TWO LANING WITH PS OF CHHAPRA - GOPALGANJ - [N24000521]NHAI, BIHAR	08/2015	854.80 -	- -	-
707	TWO LANING WITH PS OF CHHAPRA - REWAGHAT - MUZAFFARPUR - [N24000522]NHAI, BIHAR	08/2015	516.13 -	04/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
708	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-
709	MEERUT-BULANDSHAHAH - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	- -	-
710	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 -	06/2019 -	-
711	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 -	07/2018 -	-
712	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	04/2019 -	-
713	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	11/2018 -	-
714	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	02/2019 -	-
715	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-
716	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 -	03/2019 -	-
717	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-
718	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	04/2019 -	-
719	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI,WEST BENGAL	03/2016	229.37 -	11/2018 -	-
720	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	04/2019 -	-
721	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	- -	-
722	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	- -	-
723	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	-
724	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	- -	-
725	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	- -	-
726	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	- -	-
727	FOUR LANING OF TALAJA - MAHUA SECTION OF NH - 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT	05/2016	834.64 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
728	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	- -	-
729	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	- -	-
730	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	-
731	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN	06/2016	763.23 -	06/2019 -	-
732	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	06/2019 -	-
733	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	-
734	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 -	- -	-
735	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	-
736	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	10/2018 -	-
737	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	- -	-
738	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	04/2019 -	-
739	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 -	09/2019 -	-
740	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 -	- -	-
741	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH	08/2016	227.49 -	01/2019 -	-
742	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	-
743	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	08/2018 -	-
744	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	05/2019 -	-
745	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-
746	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL	09/2016	767.03 -	08/2018 -	-
747	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 -	08/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (April 2021)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
748	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA	09/2016	1,004.67 -	05/2019 -	-
749	SIX LANNING FROM EXISTING KM 494.410(DSIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DSIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	- -	-
750	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-
751	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT	12/2016	417.19 -	- -	-
752	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI, UTTAR PRADESH	12/2016	534.55 -	- -	-
753	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	07/2018 -	-
754	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI, UTTAR PRADESH	01/2017	450.68 -	- -	-
755	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI, GUJARAT	01/2017	1,251.11 -	- -	-
756	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	05/2019 -	-
757	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 -	02/2020 -	-
758	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI, UTTAR PRADESH	03/2017	1,373.28 -	03/2020 -	-
759	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI, UTTAR PRADESH	03/2017	1,184.71 -	03/2020 -	-
760	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA	03/2017	247.02 -	03/2020 -	-
761	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA	03/2017	744.64 -	03/2020 -	-
762	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	03/2020 -	-
763	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	03/2020 -	-
764	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	-
765	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA	03/2017	296.19 -	03/2020 -	-
766	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	03/2020 -	-
767	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI, UTTAR PRADESH	03/2017	1,989.00 -	03/2020 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
768	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR	03/2017	672.89 -	03/2020 -	-
769	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	-
770	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH	03/2017	2,064.99 -	03/2020 -	-
771	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	03/2020 -	-
772	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	03/2020 -	-
773	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	-
774	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	10/2017 -	-
775	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH	09/2017	374.40 -	09/2017 -	-
776	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	-
777	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGPUR ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	- -	-
778	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	- -	-
779	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	- -	-
780	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	- -	-
781	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-
782	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- -	-
783	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-
784	REHABILITATION AND UPGRADEATION OF TWO LANING OF MAHESHKUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 -	- -	-
785	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-
786	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (April 2021)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
787	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-
788	FOUR LANING OF DELINKED STRETCH OF SEONI - MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH	01/2018	960.24 -	- -	-
789	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA	01/2018	633.68 -	- -	-
790	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 -	- -	-
791	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA	03/2017	4,429.00 -	03/2017 -	-
792	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA	02/2018	486.78 -	- -	-
793	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 -	- -	-
794	FOR REHABILITATION AND UPGRADE FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 -	- -	-
795	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 -	- -	-
796	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 -	- -	-
797	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH	03/2018	925.40 -	- -	-
798	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN	02/2018	741.86 -	- -	-
799	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN	02/2018	716.76 -	- -	-
800	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	-
801	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 -	- -	-
802	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH	03/2018	1,025.80 -	- -	-
803	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH	03/2018	1,115.28 -	- -	-
804	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K - [N24000804]NHAI,TELANGANA	03/2018	802.65 -	- -	-
805	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
806	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-
807	CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	- -	-
808	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	- -	-
809	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA	03/2018	950.63 -	- -	-
810	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA	03/2018	857.62 -	- -	-
811	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI,TELANGANA	03/2018	828.29 -	- -	-
812	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU	03/2018	633.55 -	- -	-
813	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU	03/2018	2,065.96 -	- -	-
814	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE	03/2018	1,294.47 -	- -	-
815	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE	03/2018	998.70 -	- -	-
816	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT	03/2018	1,161.39 -	- -	-
817	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA	03/2018	275.12 -	- -	-
818	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXIST - [N24000837]NHAI,HARYANA	03/2018	307.79 -	- -	-
819	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN	03/2018	874.25 -	- -	-
820	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN	03/2018	1,158.35 -	- -	-
821	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB	03/2018	199.90 -	- -	-
822	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB	03/2018	196.05 -	- -	-
823	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA	03/2018	198.05 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
824	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA	03/2018	181.78 -	- -	-
825	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA	03/2018	551.58 -	- -	-
826	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA	03/2018	642.13 -	- -	-
827	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 -	- -	-
828	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - [N24001185]NHAI,UTTAR PRADESH	11/2017	2,159.00 -	01/2019 -	-
829	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI,HARYANA	01/2019	1,051.91 -	- -	-
830	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI,HARYANA	01/2019	1,120.06 -	- -	-
831	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA	01/2019	1,137.42 -	- -	-
832	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA	01/2019	1,033.19 -	- -	-
833	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA	01/2019	1,243.45 -	- -	-
834	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA	01/2019	889.36 -	- -	-
835	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA	01/2019	1,018.79 -	- -	-
836	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA	01/2019	996.65 -	- -	-
837	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214]NHAI,MADHYA PRADESH	12/2017	217.96 -	- -	-
838	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T - [N24001234]NHAI,MADHYA PRADESH	02/2019	996.27 -	03/2020 -	-
839	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105 - [N24001298]NHAI,ANDHRA PRADESH	09/2018	597.67 -	01/2020 -	-
840	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN - [N24001299]NHAI,ANDHRA PRADESH	09/2018	617.41 -	02/2019 -	-
841	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300]NHAI,ANDHRA PRADESH	11/2019	1,226.88 -	02/2021 -	-
842	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - [N24001301]NHAI,ANDHRA PRADESH	11/2019	1,601.10 -	02/2021 -	-
843	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT - [N24001303]NHAI,BIHAR	10/2013	649.90 -	12/2020 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
844	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE - [N24001304]NHAI,BIHAR	10/2013	446.97 -	11/2020 -	-
845	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA - [N24001305]NHAI,BIHAR	10/2013	464.09 -	11/2020 -	-
846	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	-
	Total		4,03,696.02 -		
	<u>URBAN DEVELOPMENT</u>				
	<u>Central Public Works Department</u>				
847	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	12/2015 -	-
848	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	12/2013 -	-
849	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD,DELHI	11/2017	238.56 -	05/2020 -	-
850	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI - [N28000123]CPWD,DELHI	07/2017	218.72 -	11/2020 -	-
851	C/O STEEL STRUCTURE BUILDINGS USING PRE-ENGINEERED TECHNOLOGY AT AFRICA AVENUE AND KG MARG - [N28000143]CPWD,DELHI	02/2020	532.00 -	11/2020 -	-
852	CONSTRUCTION 729 QUARTERS (TYPE II-180, TYPE III-364, TYPE IV-112,TYPE V-68, TYPE-VI-5), SHOPS,CO - [N28000149]CPWD,CHHATISGARH	05/2019	299.97 -	09/2020 -	-
	<u>Chennai Metro Rail Ltd</u>				
853	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU	06/2016	3,770.00 -	03/2018 -	03/2021
854	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 -	12/2015 -	-
	<u>Kochi Metro Rail Corporation Ltd</u>				
855	KOCHI METRO RAIL PROJECT - [N28000081]KMRL,KERALA	07/2012	5,181.79 -	07/2017 -	09/2020
	<u>Lucknow Metro Rail Corporation Limited</u>				
856	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	-
	<u>Nagpur Metro Rail Corporation Ltd</u>				
857	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	-
	<u>National Building Construcion Corporation Ltd</u>				
858	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI	06/2012	4,264.00 -	11/2019 -	-
	Total		45,711.60 -		

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (April 2021)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>WATER RESOURCES</u>				
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>				
859	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]BUIDCO,BIHAR	12/2014	225.77 -	03/2020 -	03/2021
860	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO,BIHAR	10/2017	254.13 -	09/2020 -	-
861	SAIDPUR SEWER NETWORK PATNA - [N30000039]BUIDCO,BIHAR	04/2015	268.63 -	01/2021 -	-
862	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]BUIDCO,BIHAR	05/2017	191.62 -	11/2020 03/2021	-
	<u>Delhi Jal Board</u>				
863	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018]DJB,DELHI	05/2017	344.81 -	05/2020 -	-
	<u>Hindustan Steelwork Construction Limited</u>				
864	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	03/2015 -	-
	<u>Kolkata Metropolitan Development Authority</u>				
865	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]KMDA,WEST BENGAL	12/2014	272.32 -	04/2020 -	03/2021
	<u>Uttar Pradesh Jal Nigam</u>				
866	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020]UPJalNigam,UTTAR PRADESH	02/2011	279.91 330.05	12/2019 -	01/2021
867	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA - [N30000011]UPJalNigam,UTTAR PRADESH	02/2017	161.31 -	11/2019 -	03/2021
868	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR - [N30000009]UPJalNigam,UTTAR PRADESH	10/2016	370.40 430.49	08/2020 03/2021	-
	<u>Uttarakhand Pey Jal Nigam</u>				
869	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI - [N30000003]UKJalNigam,UTTARAKHAND	03/2017	273.37 -	08/2019 -	-
870	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH - [N30000004]UKJalNigam,UTTARAKHAND	03/2017	158.00 -	11/2019 03/2021	-
	Total		3,756.27 -		
	<u>COMMERCE</u>				
	<u>National Building Construcion Corporation Ltd</u>				
871	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI - [N40000003]NBCC,DELHI	06/2018	302.64 -	10/2020 -	-
	Total		302.64 -		
	<u>HUMAN RESOURCE DEVELOPMENT</u>				
	<u>Central Public Works Department</u>				
872	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	11/2014 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
873	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	10/2012 -	-
874	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN	12/2016	549.31 -	07/2019 -	-
875	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133]CPWD,ANDHRA PRADESH	02/2019	186.00 199.00	09/2020 -	-
876	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED - [N28000146]CPWD,WEST BENGAL	03/2020	193.83 -	06/2020 -	-
877	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA. - [N42000002]CPWD,GOA	05/2019	303.90 -	03/2020 -	-
878	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE - [N42000005]CPWD,ANDHRA PRADESH	02/2019	655.34 -	06/2020 -	-
	<u>Edcil(India) Limited</u>				
879	STUDY IN INDIA - [N42000003]EDCIL,MULTI STATE	03/2018	150.00 -	04/2018 -	-
	<u>Indian Institute Of Technology, Kharagpur</u>				
880	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION - [N42000004]IITKGP,MULTI STATE	08/2018	418.00 -	03/2019 -	-
	<u>Rail India Technical And Economic Service</u>				
881	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]RITES,MEGHALAYA	09/2013	484.32 -	09/2014 -	-
	Total		3,376.76 -		
	<u>CULTURE DEVELOPMENT</u>				
	<u>Hindustan Steelwork Construction Limited</u>				
882	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	09/2017 -	03/2021
	Total		151.33 -		
	Grand Total		6,75,874.83		

Details of Projects Without Milestones w.r.t. Original Schedule

Annexure - X

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
	<u>Airport Authority Of India Limited</u>					
1	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA - [N04000080]AAI, WEST BENGAL	01/2016	458.00 -	03/2020 12/2021	12/2021	0/0
2	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPORT - [N04000076]AAI, DELHI	11/2016	303.80 351.21	04/2020 -	03/2022	0/0
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]AAI, ASSAM	12/2016	1,142.00 -	03/2021 03/2022	03/2022	0/0
4	CCS INTERNATIONAL AIRPORT, LUCKNOW - [N04000077]AAI, UTTAR PRADESH	06/2018	1,383.00 -	09/2021 -	09/2022	0/0
	<u>COAL</u>					
	<u>Bharat Coking Coal Limited</u>					
5	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]BCCL, WEST BENGAL	12/2015	304.13 341.22	03/2017 -	03/2022	0/0
6	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]BCCL, JHARKHAND	10/2015	243.00 334.27	04/2018 -	06/2022	0/0
	<u>Eastern Coal Fields Limited</u>					
7	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT - [N06000191]ECL, WEST BENGAL	04/2020	483.65 -	03/2025 -	03/2025	0/0
	<u>Neyveli Lignite Corporation</u>					
8	HADLA LIGNITE MINE PROJECT (1.90 MTPA) - [N06000144]NLC, RAJASTHAN	03/2015	522.45 -	09/2019 -	-	0/0
9	BARSINGSAR THERMAL POWER STATION EXTENSION - [N06000187]NLC, RAJASTHAN	03/2015	2,112.60 -	09/2020 -	-	0/0
10	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188]NLC, RAJASTHAN	03/2015	2,196.30 -	09/2020 -	-	0/0
11	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC, RAJASTHAN	03/2015	513.63 -	12/2019 -	-	0/0
	<u>South-Eastern Coal Fields Limited</u>					
12	JAMPALI OCP RCE - [N06000198]SECL, CHHATISGARH	05/2020	278.64 -	03/2024 -	03/2024	0/0
13	BAROUD OC EXPANSION (3-10 MTY) - [N06000197]SECL, CHHATISGARH	08/2020	2,309.80 -	03/2029 -	03/2029	0/0
14	PORDA CHINTAPANI OCP (10 MTY) - [N06000199]SECL, CHHATISGARH	12/2020	2,310.12 -	03/2029 -	03/2029	0/0
15	DIPKA OC EXPANSION 40 MTY - [N06000200]SECL, CHHATISGARH	12/2020	5,241.40 -	03/2029 -	03/2029	0/0
	<u>Western Coal Fields Limited</u>					
16	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL, MAHARASHTRA	03/2017	362.73 -	03/2020 -	09/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
17	RPR FOR JAMUNIA UG (0.90 MTY) - [N06000153]WCL,MADHYA PRADESH	07/2016	281.25 -	03/2022 -	03/2026	0/0
	<u>STEEL</u>					
	<u>Steel Authority Of India Limited (Sail)</u>					
18	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP - [N12000123]SAIL,CHHATISGARH	11/2020	542.24 -	12/2023 -	12/2023	0/0
	<u>PETROLEUM</u>					
	<u>Bharat Petroleum Corporation Limited</u>					
19	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY - [N16000397]BPCL,MAHARASHTRA	07/2020	640.00 -	12/2021 -	12/2021	0/0
20	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA	12/2015	1,112.00 1,507.24	06/2019 -	02/2022	0/0
21	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]BPCL,JHARKHAND	11/2018	248.55 -	06/2022 -	06/2022	0/0
22	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 1,472.00	02/2017 08/2022	08/2022	0/0
23	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]BPCL,KERALA	09/2018	11,130.00 -	03/2023 -	03/2023	0/0
24	KEROSENE HYDROTREATER (KHT) UNIT INTEGRATED WITH EXISTING DIESEL HYDROTREATER (DHT) UNIT AT MUMBAI R - [N16000410]BPCL,MAHARASHTRA	08/2020	697.00 -	03/2023 -	03/2023	0/0
	<u>Chennai Petroleum Corporation Limited</u>					
25	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU	08/2017	421.00 -	08/2020 -	09/2021	0/0
26	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU	09/2017	1,858.00 -	12/2019 -	-	0/0
	<u>Hindustan Petroleum Corporation Limited</u>					
27	SULPHUR FORMING UNIT IN SRU - [N16000408]HPCL,ANDHRA PRADESH	10/2020	210.94 -	08/2021 -	08/2021	0/0
28	RUF PITCH LOADING GANTRY - [N16000406]HPCL,ANDHRA PRADESH	10/2020	332.61 -	11/2022 -	11/2022	0/0
29	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS - [N16000385]HPCL,HARYANA	09/2018	520.00 -	09/2026 02/2027	02/2027	0/0
30	CITY GAS DISTRIBUTION IN UP AND UK - [N16000387]HPCL,UTTAR PRADESH	03/2019	3,450.20 -	03/2029 08/2029	08/2029	0/0
31	CITY GAS DISTRIBUTION IN WEST BENGAL - [N16000392]HPCL,WEST BENGAL	03/2019	5,830.20 -	03/2031 08/2029	08/2029	0/0
32	220 KV GRID SUPPLY - [N16000407]HPCL,ANDHRA PRADESH	10/2020	303.40 -	03/2021 -	-	0/0
	<u>Indian Oil Corporation Limited</u>					
33	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]IOCL,ANDHRA PRADESH	08/2017	384.58 -	04/2021 03/2021	03/2021	0/0
34	ADDITIONAL FACILITIES AT MANMAD FOR COVERION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00 -	01/2021 -	09/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
35	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL,MAHARASHTRA	05/2016	261.00 -	01/2021 -	09/2021	0/0
36	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]IOCL,MADHYA PRADESH	08/2017	236.00 293.00	06/2020 09/2021	09/2021	0/0
37	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 -	01/2021 -	10/2021	0/0
38	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]IOCL,HARYANA	08/2019	1,255.00 -	10/2021 -	10/2021	0/0
39	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	08/2021 -	11/2021	0/0
40	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH	08/2018	466.00 -	04/2021 12/2021	12/2021	0/0
41	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]IOCL,BIHAR	04/2018	522.00 -	03/2021 12/2021	12/2021	0/0
42	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	10/2020 01/2022	01/2022	0/0
43	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]IOCL,ANDHRA PRADESH	10/2018	316.20 -	10/2021 03/2022	03/2022	0/0
44	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383]IOCL,HARYANA	09/2019	164.69 -	07/2021 03/2022	03/2022	0/0
45	LPG BP PROJECT CHITTOOR - [N16000381]IOCL,ANDHRA PRADESH	07/2019	167.00 -	07/2022 -	07/2022	0/0
46	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY - [N16000395]IOCL,ODISHA	01/2020	202.16 -	07/2022 -	07/2022	0/0
47	MUZAFFARPUR-MOTIHARI LPG PIPELINE - [N16000399]IOCL,BIHAR	06/2020	403.00 -	08/2022 -	08/2022	0/0
48	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400]IOCL,GUJARAT	06/2020	1,378.00 -	12/2022 -	12/2022	0/0
49	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY - [N16000393]IOCL,WEST BENGAL	06/2020	1,019.00 -	01/2023 -	01/2023	0/0
50	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	04/2022 -	02/2023	0/0
51	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI - [N16000405]IOCL,TAMIL NADU	10/2020	1,398.00 -	12/2023 -	05/2023	0/0
52	R and D CAMPUS II AT FARIDABAD - [N16000375]IOCL,HARYANA	06/2019	2,281.94 -	12/2022 07/2023	07/2023	0/0
53	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA	12/2018	611.00 -	04/2022 -	08/2023	0/0
54	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM - [N16000411]IOCL,GUJARAT	10/2020	1,614.00 -	08/2023 -	08/2023	0/0
55	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI - [N16000403]IOCL,TAMIL NADU	10/2020	921.00 -	09/2023 -	09/2023	0/0
56	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY - [N16000396]IOCL,ODISHA	07/2020	13,805.00 -	01/2024 -	01/2024	0/0
57	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY - [N16000409]IOCL,GUJARAT	09/2020	18,936.00 -	09/2024 -	09/2024	0/0
58	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	06/2020 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	<u>Numaligarh Refinery Limited</u>					
59	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY - [N16000379]NRL, ASSAM	01/2019	12,366.00 -	10/2024 -	10/2024	0/0
60	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES - [N16000394]NRL, ASSAM	01/2019	10,228.00 -	10/2024 -	10/2024	0/0
	<u>Oil & Natural Gas Corporation Limited</u>					
61	REDEVELOPMENT OF NANDASAN FIELD - [N16000404]ONGC, GUJARAT	02/2020	444.87 -	08/2022 -	08/2022	0/0
	<u>Oil India Limited</u>					
62	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN - [N16000356]OIL, ASSAM	06/2016	224.75 -	08/2020 -	06/2021	0/0
	<u>POWER</u>					
	<u>Central Public Works Department</u>					
63	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD, DELHI	10/2017	271.90 -	11/2019 -	06/2021	0/0
	<u>Chenab Valley Power Projects [P] Limited</u>					
64	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL, JAMMU AND KASHMIR	10/2014	8,112.12 -	04/2020 -	07/2025	0/0
	<u>National Hydro-Electric Power Corporation</u>					
65	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC, ARUNACHAL PRADESH	09/2003	6,285.33 19,992.43	09/2010 08/2023	08/2023	0/0
66	LOKTAK D/S HEP (NHPC) - [180100078]NHPC, MANIPUR	12/1999	578.62 -	06/2006 -	-	0/0
	<u>National Thermal Power Corporation</u>					
67	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000273]NTPC, UTTAR PRADESH	12/2018	587.44 -	09/2020 -	01/2021	0/0
68	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000274]NTPC, UTTAR PRADESH	03/2019	349.00 -	11/2020 -	04/2021	0/0
69	RAMAGUNDAM FLOATING SOLAR 100 MW - [N18000284]NTPC, TELANGANA	06/2019	401.90 -	04/2021 -	04/2021	0/0
70	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC, ODISHA	05/2016	1,885.13 -	12/2018 -	07/2021	0/0
71	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC, WEST BENGAL	12/2016	529.68 -	11/2018 -	07/2021	0/0
72	FATEHGARH SOLAR 296MW - [N18000289]NTPC, RAJASTHAN	03/2020	1,749.31 -	09/2021 -	09/2021	0/0
73	ETTAYAPURAM SOLAR 230MW - [N18000290]NTPC, TAMIL NADU	03/2020	1,316.22 -	09/2021 -	09/2021	0/0
74	KAWAS SOLAR 56 MW - [N18000283]NTPC, GUJARAT	08/2020	261.80 -	10/2021 -	10/2021	0/0
75	KAYAMKULAM SOLAR 70 MW - [N18000288]NTPC, KERALA	09/2019	403.62 -	06/2021 10/2021	10/2021	0/0
76	DEVIKOT SOLAR 90MW - [N18000280]NTPC, UTTAR PRADESH	03/2020	501.29 -	09/2021 01/2022	01/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
77	DEVIKOT SOLAR 150MW - [N18000281]NTPC,UTTAR PRADESH	01/2020	798.24 -	09/2021 01/2022	01/2022	0/0
78	NOKHRA - [N18000282]NTPC,UTTAR PRADESH	03/2020	1,722.14 -	09/2021 01/2022	01/2022	0/0
79	SAMBHU KI BHURJ SOLAR 250 MW - [N18000285]NTPC,RAJASTHAN	01/2020	1,522.71 -	09/2021 01/2022	01/2022	0/0
80	SAMBHU KI BHURJ-II SOLAR 300MW - [N18000286]NTPC,RAJASTHAN	03/2020	1,782.00 -	09/2021 01/2022	01/2022	0/0
81	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,238.00	10/2017 -	-	0/0
82	TALAIPELLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH	09/2015	3,004.00 -	11/2019 -	-	0/0
83	JETSAR SOLAR 160 MW - [N18000287]NTPC,RAJASTHAN	12/2019	702.28 -	03/2021 -	-	0/0
	<u>Power Grid Corporation Of India Limited</u>					
84	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE	10/2016	408.46 516.12	01/2019 09/2020	04/2020	0/0
85	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE	09/2017	198.49 -	09/2019 09/2020	05/2020	0/0
86	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT	05/2017	175.64 -	09/2018 11/2020	09/2020	0/0
87	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT	12/2017	193.14 -	06/2019 11/2020	09/2020	0/0
88	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA	05/2017	445.89 675.73	02/2019 02/2021	02/2021	0/0
89	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	01/2018 04/2021	05/2021	0/0
90	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL	04/2016	454.11 -	04/2018 03/2021	05/2021	0/0
91	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE	11/2017	358.83 -	05/2020 05/2021	05/2021	0/0
92	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	04/2016 12/2017	06/2021	0/0
93	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	03/2018 -	06/2021	0/0
94	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE	05/2016	14,733.37 -	11/2019 04/2021	06/2021	0/0
95	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	06/2019 08/2021	06/2021	0/0
96	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL,MULTI STATE	02/2017	5,070.13 -	04/2020 06/2021	06/2021	0/0
97	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE	03/2017	3,500.00 3,500.00	07/2020 12/2020	06/2021	0/0
98	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 219.66	07/2019 04/2021	06/2021	0/0
99	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALAR EN - [N18000264]PGCIL,MULTI STATE	08/2017	1,931.39 -	02/2020 06/2021	06/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
100	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE	02/2017	322.30 -	02/2019 06/2021	09/2021	0/0
101	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE	03/2017	379.95 -	12/2019 06/2021	09/2021	0/0
102	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 6,700.00	12/2018 -	12/2021	0/0
103	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 9,129.32	12/2018 -	03/2024	0/0
104	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE	05/2016	3,519.59 -	05/2019 -	-	0/0
105	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE	03/2017	283.72 -	11/2019 -	-	0/0
106	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE	10/2016	608.24 -	04/2019 -	-	0/0
107	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE	12/2015	3,654.00 -	04/2019 -	-	0/0
	<u>Satluj Jal Vidyut Nigam Limited</u>					
108	LUHRI HYDROELECTRIC PROJECT (STAGE1) - [N18000279]SJVN,HIMACHAL PRADESH	11/2020	1,810.56 -	01/2026 -	01/2026	0/0
	<u>HEAVY INDUSTRY</u>					
	<u>Bharat Heavy Electricals Limited</u>					
109	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL,DELHI	08/2016	1,554.00 -	09/2019 -	-	0/0
	<u>HEALTH AND FAMILY WELFARE</u>					
	<u>Central Public Works Department</u>					
110	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD,HIMACHAL PRADESH	12/2018	260.00 -	06/2021 -	05/2022	0/0
111	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR - [N21000029]CPWD,JAMMU AND KASHMIR	03/2019	1,404.00 -	09/2023 -	09/2023	0/0
112	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150]CPWD,JAMMU AND KASHMIR	03/2019	1,828.00 -	09/2025 -	05/2024	0/0
113	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]CPWD,JAMMU AND KASHMIR	03/2019	1,577.00 -	09/2025 -	09/2025	0/0
	<u>HII Infra Tech Services Limited</u>					
114	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	04/2020 -	07/2021	0/0
115	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	06/2020 -	07/2021	0/0
116	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 -	05/2021 -	07/2022	0/0
	<u>Hospital Services Consultancy Corporation Ltd</u>					
117	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	03/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
118	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC, WEST BENGAL	08/2016	244.00 -	09/2018 -	05/2019	0/0
119	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASHTRA - [N21000016]HSCC, MAHARASHTRA	08/2017	274.19 -	03/2019 -	01/2021	0/0
120	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC, GOA	01/2018	249.01 -	- -	01/2021	0/0
121	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC, ANDHRA PRADESH	08/2017	272.19 -	03/2019 -	03/2021	0/0
122	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC, UTTAR PRADESH	03/2018	268.84 -	- -	03/2021	0/0
123	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC, DELHI	02/2013	414.11 -	11/2013 -	05/2021	0/0
124	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC, WEST BENGAL	08/2017	355.15 -	03/2019 -	06/2021	0/0
125	GERIATRICS BLOCK- AIIMS DELHI - [N21000019]HSCC, DELHI	12/2017	156.56 -	- -	06/2021	0/0
126	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC, ANDHRA PRADESH	03/2018	601.02 -	- -	06/2021	0/0
127	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC, MAHARASHTRA	03/2018	582.99 -	- -	06/2021	0/0
128	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC, WEST BENGAL	04/2018	651.99 -	- -	06/2021	0/0
129	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC, MEGHALAYA	10/2016	363.99 -	05/2018 -	12/2021	0/0
	<u>RAILWAYS</u>					
	<u>Central Railways</u>					
130	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR, MAHARASHTRA	02/1997	2,271.50 -	03/2021 -	03/2023	0/0
131	WARDHA-NANDED MAHARASHTRA - [N22000231]CR, MAHARASHTRA	04/2008	3,168.29 -	03/2023 -	03/2023	0/0
132	KALYAN-KASARA 3RD LINE - [N22000233]CR, MAHARASHTRA	04/2011	792.89 -	03/2021 -	03/2023	0/0
133	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR, MAHARASHTRA	02/2015	1,272.19 -	03/2022 -	03/2023	0/0
134	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR, MAHARASHTRA	02/2015	3,627.47 3,627.00	03/2024 -	03/2023	0/0
135	DAUND - MANMAD (236 KM) - [N22000360]CR, MAHARASHTRA	02/2016	1,876.00 -	03/2023 -	03/2023	0/0
136	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR, MAHARASHTRA	04/2012	540.02 -	03/2022 -	03/2024	0/0
137	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR, MAHARASHTRA	02/2016	9,968.00 -	03/2024 -	03/2024	0/0
138	PUNE-NASIK (265 KM) - [N22000354]CR, MAHARASHTRA	02/2016	2,425.00 -	03/2024 -	03/2024	0/0
139	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]CR, MAHARASHTRA	02/2016	2,750.00 -	03/2024 -	03/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
140	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,449.91 -	03/2023 -	03/2024	0/0
141	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 -	03/2022 -	03/2024	0/0
142	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 -	03/2023 -	03/2024	0/0
143	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	03/2019 -	-	0/0
	<u>Container Corporation Of India</u>					
144	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH	01/2013	387.70 -	03/2018 -	03/2021	0/0
145	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00 -	03/2019 -	12/2020	0/0
146	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32 -	03/2019 -	03/2021	0/0
147	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	03/2018 -	-	0/0
148	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH	05/2014	207.00 -	03/2018 -	-	0/0
149	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	03/2019 -	-	0/0
150	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	03/2019 -	-	0/0
151	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	03/2019 -	-	0/0
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>					
152	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	11,589.00 30,357.00	- -	-	0/0
153	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE	11/2007	16,592.00 51,101.00	03/2020 -	-	0/0
	<u>East Central Railways</u>					
154	SAKRI-HASANPUR ROAD (NL) - [N22000171]JECR,BIHAR	04/1999	325.00 -	- -	03/2021	0/0
155	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]JECR,BIHAR	04/1996	477.88 283.95	03/2012 -	07/2021	0/0
156	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]JECR,JHARKHAND	03/1999	1,033.07 -	- -	03/2022	0/0
157	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]JECR,UTTAR PRADESH	08/2015	528.57 -	03/2019 -	03/2022	0/0
158	GARHWA ROAD-RAMNA - [N22000465]JECR,JHARKHAND	03/2015	348.23 -	03/2021 -	03/2022	0/0
159	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIAWAN-BIHARSHARIF, - [N22000476]JECR,BIHAR	04/1991	329.39 -	- -	03/2022	0/0
160	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]JECR,BIHAR	04/2016	731.64 -	03/2021 -	06/2022	0/0
161	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]JECR,BIHAR	04/1997	324.73 -	03/2012 -	11/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
162	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	03/2023	0/0
163	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	03/2023	0/0
164	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR	04/2006	378.56 -	- -	03/2023	0/0
165	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	1,605.17 -	- -	03/2023	0/0
166	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	03/2023	0/0
167	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	548.00 -	03/2020 -	03/2023	0/0
168	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	12/2023	0/0
169	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR	04/2008	326.20 -	- -	03/2024	0/0
170	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	03/2024	0/0
171	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	03/2020 -	03/2024	0/0
172	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 -	03/2021 -	03/2024	0/0
173	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	03/2025	0/0
174	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	499.41 -	03/2020 -	-	0/0
175	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-	0/0
176	ARA-BHABHUA ROAD (NL) - [N22000166]ECR,BIHAR	04/2008	633.87 -	- -	-	0/0
177	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-	0/0
178	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR	04/2008	445.25 -	- -	-	0/0
179	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE	04/2008	415.67 -	- -	-	0/0
180	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-	0/0
181	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-	0/0
182	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-	0/0
183	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-	0/0
184	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-	0/0
185	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
186	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR,BIHAR	04/1998	180.82 -	- -	-	0/0
	<u>East Coast Railway</u>					
187	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 -	02/2019 -	12/2021	0/0
188	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 238.03	03/2020 03/2021	03/2022	0/0
189	JAGDALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 1,547.38	03/2022 03/2023	03/2023	0/0
190	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 843.04	10/2020 03/2024	03/2024	0/0
191	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 -	03/2022 03/2024	03/2024	0/0
192	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	11/2018 -	03/2024	0/0
193	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 1,172.92	12/2018 03/2024	03/2024	0/0
194	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 1,928.07	06/2021 03/2025	03/2025	0/0
195	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 3,791.66	03/2009 03/2026	03/2026	0/0
196	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 2,361.74	03/2022 03/2026	03/2026	0/0
	<u>Eastern Railways</u>					
197	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	05/2019	0/0
198	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	03/2021	0/0
199	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	11/2018 -	03/2021	0/0
200	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	542.18 -	03/2020 -	03/2021	0/0
201	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	03/2022	0/0
202	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	03/2022	0/0
203	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	02/2013 -	03/2024	0/0
204	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	03/2024	0/0
205	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	03/2019 12/2009	03/2025	0/0
206	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	03/2006 -	03/2025	0/0
207	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	03/2025	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
208	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	03/2025	0/0
209	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	03/2022 -	03/2025	0/0
210	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	03/2016 -	03/2025	0/0
211	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.51 -	03/2017 -	03/2025	0/0
212	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	03/2025	0/0
213	SONDALIA-CHAMPAPUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	03/2016 -	03/2025	0/0
214	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	03/2017 -	03/2025	0/0
215	BARIARPIUR-MANANPUR VIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	03/2025	0/0
216	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	03/2025	0/0
217	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	03/2005 -	03/2025	0/0
218	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	03/2025	0/0
219	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	03/2025	0/0
220	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96 -	02/2012 -	03/2025	0/0
221	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2025	0/0
222	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGREGATION OF ARRIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	03/2025	0/0
223	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	03/2017 -	03/2026	0/0
<u>Indian Railway Construction Company Limited</u>						
224	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA	04/2016	5,200.00 -	03/2020 -	03/2024	0/0
<u>Kolkata Metro Rail Corporation Limited</u>						
225	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-	0/0
<u>Metropolitan Rapid Transport Projects</u>						
226	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	06/2021	0/0
227	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP, MAHARASHTRA	03/1996	495.44 -	03/2004 -	03/2022	0/0
228	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	03/2025	0/0
229	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
230	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 -	03/2014 -	-	0/0
231	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	-	0/0
	<u>North Central Railway</u>					
232	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR, UTTAR PRADESH	03/2018	4,329.53 -	03/2023 -	03/2023	0/0
233	ETAHAH-MAINPURI (NL), NCR - [220100318]NCR, UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-	0/0
234	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR, MULTI STATE	04/2010	2,030.50 -	- -	-	0/0
	<u>North East Frontier Railway</u>					
235	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR, ASSAM	04/2011	314.00 486.96	03/2019 -	03/2021	0/0
236	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR, WEST BENGAL	04/2016	602.27 -	12/2021 -	04/2021	0/0
237	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	1,180.19 2,531.34	12/2008 -	05/2021	0/0
238	DIGARU-HOJAI (102 KM) - [N22000389]NFR, ASSAM	04/2015	870.96 -	03/2021 -	05/2021	0/0
239	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR, MULTI STATE	04/2010	241.52 -	- -	12/2021	0/0
240	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	385.20 -	03/2019 -	03/2023	0/0
241	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	2,393.47 5,021.45	03/2014 -	03/2023	0/0
242	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR, ASSAM	04/2015	2,232.32 -	03/2022 -	03/2023	0/0
243	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR	04/2003	4,454.17 -	03/2011 -	12/2023	0/0
244	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR, BIHAR	09/2006	532.87 2,132.03	03/2019 -	03/2024	0/0
245	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR, MULTI STATE	04/2013	1,798.00 2,042.51	03/2019 -	03/2024	0/0
246	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND	04/2006	2,326.52 -	03/2015 -	12/2024	0/0
247	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR - [220100135]NFR, WEST BENGAL	04/1983	297.32 200.34	03/2019 -	-	0/0
248	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48 -	12/2015 -	-	0/0
249	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 -	- -	-	0/0
250	DIMAPUR-TIZIT NL - [N22000196]NFR, NAGALAND	04/2013	4,274.00 -	03/2020 -	-	0/0
251	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR, MEGHALAYA	04/2010	906.46 1,202.33	03/2021 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
252	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 -	03/2020 -	-	0/0
253	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE	04/1999	819.23 -	- -	-	0/0
254	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHOWA-JAIN - [N22000499]NFR,WEST BENGAL	02/1999	380.60 -	04/2010 -	-	0/0
255	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	333.76 -	- -	-	0/0
256	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	414.84 -	03/2020 -	-	0/0
	<u>North Eastern Railway</u>					
257	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH	04/2017	622.50 427.00	04/2017 -	03/2021	0/0
258	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	12/2019 -	04/2021	0/0
259	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	12/2021 -	12/2021	0/0
260	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	04/2016 -	12/2021	0/0
261	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	01/2019 -	02/2022	0/0
262	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH	03/2015	1,295.42 -	03/2022 -	03/2022	0/0
263	AUNRIHAR - JAUNPUR PATCH DOUBLING. - [N22000469]NER,UTTAR PRADESH	04/2016	600.00 -	01/2022 -	03/2022	0/0
264	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	04/2017 -	04/2022	0/0
265	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	04/2017 -	10/2022	0/0
266	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	12/2022 -	12/2022	0/0
267	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH	04/2016	602.50 -	- -	12/2023	0/0
268	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH	04/2016	1,900.00 -	01/2022 -	03/2025	0/0
269	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-	0/0
270	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0
271	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
272	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-	0/0
273	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-	0/0
	<u>North Western Railway</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
274	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	10/2018 -	01/2020	0/0
275	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	02/2019 -	02/2020	0/0
276	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	12/2019 -	02/2021	0/0
277	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	11/2019 -	03/2021	0/0
278	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	420.18 -	03/2020 -	06/2021	0/0
279	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	02/2019 -	06/2022	0/0
280	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	03/2020 -	10/2022	0/0
281	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	08/2022 -	11/2022	0/0
282	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0
283	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-	0/0
	<u>Northern Railway</u>					
284	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	12/2011 -	06/2021	0/0
285	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 -	03/2016 -	06/2021	0/0
286	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 -	11/2002 -	12/2022	0/0
287	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	03/2023	0/0
288	UNCHAHAH-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	1,229.00 -	- -	03/2023	0/0
289	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	09/2023	0/0
290	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	03/2024	0/0
291	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	03/2024	0/0
292	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	03/2024	0/0
293	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE	04/2007	328.14 1,540.13	03/2023 03/2025	03/2025	0/0
294	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI - [N22000502]NR,PUNJAB	06/2009	404.00 -	08/2016 -	08/2025	0/0
295	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-	0/0
	<u>National High Speed Rail Corporation Limited</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
296	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE	12/2015	1,08,000.00	12/2023	12/2023	0/0
	<u>Rail India Technical And Economic Service</u>					
297	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38	-	-	0/0
	<u>Rail Vikas Nigam Ltd.</u>					
298	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT	04/2012	644.38	03/2021	03/2021	0/0
299	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT	04/2012	975.62	12/2021	12/2021	0/0
300	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68	03/2016	12/2021	0/0
301	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	713.48	03/2020	12/2021	0/0
302	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	948.04	03/2020	12/2021	0/0
303	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	1,402.02	03/2020	12/2021	0/0
304	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH	04/2011	1,485.85	12/2020	12/2021	0/0
305	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,548.66	12/2021	03/2022	0/0
306	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71	03/2020	03/2022	0/0
307	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70	02/2015	06/2022	0/0
308	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01	03/2019	06/2022	0/0
309	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95	03/2019	06/2022	0/0
310	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25	12/2020	12/2022	0/0
311	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH	04/2015	3,246.26	12/2023	12/2023	0/0
312	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501]RVNL,UTTAR PRADESH	06/2016	3,677.76	12/2023	12/2023	0/0
313	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60	03/2022	12/2024	0/0
314	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA	04/2015	773.94	12/2024	12/2024	0/0
315	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92	03/2023	12/2024	0/0
316	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98	03/2016	03/2025	0/0
317	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51	03/2016	03/2025	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
318	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00	12/2024	03/2025	0/0
319	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA	04/2015	723.78	12/2025	03/2025	0/0
320	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42	03/2014	12/2025	0/0
321	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH	04/2008	2,966.99	12/2026	12/2025	0/0
322	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA	01/1991	2,335.67	12/2024	12/2026	0/0
323	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	1,185.64	12/2017	-	0/0
<u>Railway Electrification</u>						
324	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10	03/2012	-	0/0
<u>South Central Railway</u>						
325	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA	04/2017	119.73 185.00	03/2022	12/2022	0/0
326	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 1.00	03/2000	03/2023	0/0
327	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20	03/2009	03/2024	0/0
328	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95	03/2023	03/2024	0/0
329	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03	03/2021	03/2024	0/0
330	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00	03/2022	03/2024	0/0
331	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	164.36	02/2009	-	0/0
332	GUDUR-DURGARAJPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	761.37	-	-	0/0
333	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07	-	-	0/0
<u>South East Central Railway</u>						
334	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH	04/2015	1,370.00	12/2021	12/2023	0/0
335	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79	-	-	0/0
336	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR,CHHATISGARH	04/2008	872.00	12/2019	-	0/0
<u>South Eastern Railway</u>						
337	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77	12/2016	08/2020	0/0
338	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 358.68	12/2018 12/2018	04/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
339	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 1,312.96	03/2020 03/2020	12/2021	0/0
340	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	03/2021 03/2021	12/2023	0/0
341	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- -	03/2025	0/0
342	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	651.00 -	03/2015 -	03/2025	0/0
343	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 1,966.70	03/2003 -	03/2030	0/0
344	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-	0/0
345	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-	0/0
	<u>South Western Railway</u>					
346	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	03/2020 -	06/2021	0/0
347	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01 -	- -	12/2023	0/0
348	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	12/2023	0/0
349	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	12/2023	0/0
350	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	348.85 -	- -	12/2023	0/0
351	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	12/2023	0/0
352	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	12/2023	0/0
353	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 -	03/2016 -	12/2023	0/0
354	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 -	03/2002 -	03/2024	0/0
355	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	03/2016 -	03/2024	0/0
356	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 -	03/2019 03/2024	03/2024	0/0
357	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00 -	- -	12/2024	0/0
358	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 -	03/2017 03/2025	03/2025	0/0
359	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 -	12/2018 -	06/2025	0/0
	<u>Southern Railway</u>					
360	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU	10/2013	187.26 -	04/2014 -	12/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
361	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	931.98 -	- 05/2021	05/2021	0/0
362	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- 10/2021	09/2021	0/0
363	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	03/2005 -	09/2021	0/0
364	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	12/2021	0/0
365	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU	02/2015	1,700.00 -	03/2022 -	06/2022	0/0
366	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU	02/2015	760.00 -	03/2020 -	06/2022	0/0
367	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	03/2024	0/0
368	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	03/2024	0/0
369	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	03/2020 -	03/2025	0/0
370	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	02/2019 -	03/2025	0/0
371	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	- -	12/2025	0/0
372	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	03/2024 -	03/2026	0/0
373	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	03/2019 -	12/2027	0/0
374	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	1,566.00 -	- -	-	0/0
375	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	227.40 -	- -	-	0/0
376	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	151.84 -	02/2019 -	-	0/0
377	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-	0/0
378	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-	0/0
379	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-	0/0
380	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-	0/0
381	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 -	- -	-	0/0
382	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	- -	-	0/0
383	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-	0/0
384	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU	02/1999	257.00 257.00	03/2018 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>Western Railway</u>					
385	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT	04/2017	691.84 1,017.91	03/2020 02/2021	02/2021	0/0
386	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT	02/1991	551.51 890.76	03/2019 10/2021	10/2021	0/0
387	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	1,037.15 1,389.05	03/2021 12/2021	12/2021	0/0
388	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 1,002.39	03/2021 12/2022	12/2022	0/0
389	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 411.62	03/2012 03/2023	03/2023	0/0
390	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 1,347.26	03/2022 03/2023	03/2023	0/0
391	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 1,640.04	03/2022 03/2023	03/2023	0/0
392	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 1,378.11	03/2019 03/2023	03/2023	0/0
393	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH	04/2016	700.00 603.69	06/2020 03/2023	03/2023	0/0
394	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	3,503.69 5,912.40	03/2022 03/2024	03/2024	0/0
395	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	829.74 1,959.74	03/2020 03/2024	03/2024	0/0
396	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	844.10 844.10	- 03/2024	03/2024	0/0
397	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-	0/0
398	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT	03/2017	243.60 -	- -	-	0/0
399	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-	0/0
400	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-	0/0
401	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-	0/0
402	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 -	- -	-	0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
	<u>Central Public Works Department</u>					
403	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE - [N24001236]CPWD,TAMIL NADU	03/2019	297.55 -	11/2019 -	-	0/0
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>					
404	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH	01/2012	410.72 -	04/2015 -	03/2021	0/0
405	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MoRTH,RAJASTHAN	03/2019	178.13 -	- -	03/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
406	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]MoRTH,MADHYA PRADESH	11/2013	497.05 -	05/2017 -	04/2021	0/0
407	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. - [N24001174]MoRTH,MANIPUR	10/2016	235.31 -	11/2020 -	11/2020	0/0
408	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]MoRTH,NAGALAND	03/2017	217.35 -	11/2020 05/2021	11/2020	0/0
409	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]MoRTH,MIZORAM	11/2010	624.41 -	03/2011 -	12/2020	0/0
410	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]MoRTH,PUNJAB	11/2015	889.24 -	- -	12/2020	0/0
411	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]MoRTH,NAGALAND	10/2016	167.62 -	12/2020 09/2021	12/2020	0/0
412	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]MoRTH,NAGALAND	10/2016	172.63 -	12/2020 09/2021	12/2020	0/0
413	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]MoRTH,WEST BENGAL	04/2014	279.70 398.52	08/2017 01/2020	02/2020	0/0
414	R AND U FROM KM 385.00 TO KM 420.000 TO 2- LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404 - [N24001205]MoRTH,UTTAR PRADESH	12/2016	209.10 -	10/2019 -	04/2020	0/0
415	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]MoRTH,CHHATISGARH	11/2015	485.44 -	12/2015 05/2020	05/2020	0/0
416	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH,ARUNACHAL PRADESH	11/2016	243.89 -	- -	09/2020	0/0
417	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 127.500 TO 178.944 DARRIGHAT TO BANARI SECTION - [N24001220]MoRTH,CHHATISGARH	03/2016	491.52 512.77	09/2016 10/2020	10/2020	0/0
418	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884]MoRTH,MADHYA PRADESH	03/2018	191.21 -	11/2019 -	01/2021	0/0
419	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131]MoRTH,JHARKHAND	03/2018	212.99 -	06/2020 -	01/2021	0/0
420	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH - [N24001145]MoRTH,UTTAR PRADESH	05/2013	164.54 165.00	08/2015 -	01/2021	0/0
421	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]MoRTH,UTTAR PRADESH	03/2018	185.18 -	02/2020 -	01/2021	0/0
422	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]MoRTH,MADHYA PRADESH	11/2017	235.91 -	02/2018 02/2021	02/2021	0/0
423	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]MoRTH,HARYANA	01/2017	247.25 -	03/2019 -	02/2021	0/0
424	REHABILITATION AND UPGRADATION OF HARPALPUR -SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942]MoRTH,UTTAR PRADESH	03/2016	208.50 -	11/2019 -	02/2021	0/0
425	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883]MoRTH,WEST BENGAL	03/2018	254.30 254.30	10/2020 -	03/2021	0/0
426	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH,UTTAR PRADESH	03/2016	240.30 240.00	01/2020 -	03/2021	0/0
427	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]MoRTH,UTTAR PRADESH	03/2016	249.50 -	05/2019 -	03/2021	0/0
428	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203]MoRTH,UTTAR PRADESH	10/2016	218.90 -	03/2020 -	03/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
429	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]MoRTH,UTTAR PRADESH	07/2016	208.88 -	10/2019 -	03/2021	0/0
430	FOUR LANE WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208]MoRTH,UTTAR PRADESH	03/2018	288.30 -	08/2020 -	03/2021	0/0
431	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO - [N24001224]MoRTH,CHHATISGARH	03/2017	423.79 -	01/2018 03/2021	03/2021	0/0
432	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]MoRTH,MADHYA PRADESH	12/2015	957.54 -	02/2020 04/2021	04/2021	0/0
433	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]MoRTH,WEST BENGAL	02/2018	218.70 218.70	11/2020 04/2020	04/2021	0/0
434	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH	11/2017	249.05 -	07/2018 03/2021	04/2021	0/0
435	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]MoRTH,MADHYA PRADESH	03/2016	877.79 -	06/2019 04/2021	04/2021	0/0
436	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]MoRTH,UTTAR PRADESH	10/2013	445.89 653.00	03/2017 -	04/2021	0/0
437	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]MoRTH,UTTAR PRADESH	03/2018	263.89 -	04/2020 -	04/2021	0/0
438	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]MoRTH,WEST BENGAL	01/2017	396.86 396.86	09/2019 11/2020	05/2021	0/0
439	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]MoRTH,MADHYA PRADESH	01/2016	809.16 -	07/2018 05/2021	05/2021	0/0
440	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH,PUNJAB	03/2018	170.57 -	11/2020 -	05/2021	0/0
441	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA	02/2017	157.32 188.00	05/2019 -	05/2021	0/0
442	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]MoRTH,UTTAR PRADESH	03/2016	296.50 -	09/2020 -	05/2021	0/0
443	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]MoRTH,CHHATISGARH	12/2015	291.05 -	- 06/2021	06/2021	0/0
444	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]MoRTH,MIZORAM	08/2010	193.69 -	10/2010 -	06/2021	0/0
445	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]MoRTH,SIKKIM	04/2013	151.59 370.01	08/2013 06/2021	06/2021	0/0
446	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]MoRTH,SIKKIM	04/2013	166.27 359.92	08/2013 06/2021	06/2021	0/0
447	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]MoRTH,SIKKIM	01/2013	182.28 369.64	02/2013 06/2021	06/2021	0/0
448	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH,MADHYA PRADESH	06/2015	390.51 -	- 03/2021	06/2021	0/0
449	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]MoRTH,MIZORAM	08/2010	195.04 -	10/2010 -	06/2021	0/0
450	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH	11/2015	628.45 -	01/2020 01/2021	06/2021	0/0
451	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH,MADHYA PRADESH	03/2015	511.83 -	08/2017 06/2021	06/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
452	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH	03/2018	162.56 -	03/2018 -	06/2021	0/0
453	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH,MADHYA PRADESH	02/2018	169.63 -	03/2018 -	06/2021	0/0
454	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]MoRTH,MADHYA PRADESH	11/2017	184.62 -	02/2018 06/2021	06/2021	0/0
455	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH	01/2017	205.05 -	03/2017 -	06/2021	0/0
456	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH	03/2018	233.04 -	03/2018 -	06/2021	0/0
457	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]MoRTH,MADHYA PRADESH	11/2017	254.17 -	02/2018 03/2021	06/2021	0/0
458	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH	02/2018	279.44 -	03/2018 12/2020	06/2021	0/0
459	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]MoRTH,MADHYA PRADESH	01/2017	373.82 -	09/2019 06/2021	06/2021	0/0
460	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]MoRTH,MAHARASHTRA	03/2016	536.65 356.00	12/2019 06/2021	06/2021	0/0
461	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MoRTH,MADHYA PRADESH	11/2017	392.33 428.55	03/2018 06/2021	06/2021	0/0
462	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]MoRTH,MIZORAM	08/2010	186.96 -	09/2014 -	06/2021	0/0
463	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]MoRTH,CHHATISGARH	01/2016	497.14 572.66	08/2016 06/2021	06/2021	0/0
464	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218]MoRTH,CHHATISGARH	11/2015	335.32 -	06/2017 06/2021	06/2021	0/0
465	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]MoRTH,CHHATISGARH	01/2016	476.20 543.73	09/2016 06/2021	06/2021	0/0
466	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]MoRTH,CHHATISGARH	01/2016	624.98 731.50	10/2016 06/2021	06/2021	0/0
467	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222]MoRTH,CHHATISGARH	03/2016	452.94 435.61	07/2016 06/2021	06/2021	0/0
468	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226]MoRTH,CHHATISGARH	12/2014	496.02 -	03/2015 06/2021	06/2021	0/0
469	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228]MoRTH,CHHATISGARH	11/2017	188.80 -	05/2019 06/2021	06/2021	0/0
470	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 - [N24001229]MoRTH,CHHATISGARH	12/2014	379.16 -	11/2017 06/2021	06/2021	0/0
471	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 KM - [N24001230]MoRTH,UTTAR PRADESH	11/2018	281.45 -	12/2020 -	06/2021	0/0
472	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]MoRTH,TRIPURA	10/2016	171.90 -	08/2020 -	07/2021	0/0
473	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905]MoRTH,PUNJAB	03/2018	322.48 -	07/2020 -	08/2021	0/0
474	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH,PUNJAB	10/2017	1,069.59 -	10/2019 -	08/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
475	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH	11/2016	326.99 327.00	- -	09/2021	0/0
476	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH	03/2018	214.69 -	03/2018 -	09/2021	0/0
477	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]MoRTH,MADHYA PRADESH	03/2018	217.22 -	08/2018 09/2021	09/2021	0/0
478	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152]MoRTH,ASSAM	09/2018	160.00 -	09/2021 -	09/2021	0/0
479	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]MoRTH,MADHYA PRADESH	11/2011	954.43 -	09/2015 -	10/2021	0/0
480	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]MoRTH,MADHYA PRADESH	01/2019	264.50 -	03/2021 11/2021	11/2021	0/0
481	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]MoRTH,WEST BENGAL	02/2018	426.18 426.18	09/2020 -	12/2021	0/0
482	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH,WEST BENGAL	06/2016	236.78 263.26	08/2019 -	12/2021	0/0
483	NAGAU-BIKANER SECTION FROM KM 177.00 TO KM 267.325 ON NH-89 - [N24001240]MoRTH,RAJASTHAN	03/2020	370.36 -	08/2022 -	08/2022	0/0
484	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGAU SECTION BY EXECUTING BALANCE WORK FRO - [N24001241]MoRTH,RAJASTHAN	03/2020	255.23 -	08/2020 -	08/2022	0/0
485	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K - [N24001242]MoRTH,RAJASTHAN	08/2020	196.23 -	11/2020 -	08/2022	0/0
486	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH,WEST BENGAL	03/2016	160.27 213.97	08/2019 -	11/2022	0/0
487	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180]MoRTH,NAGALAND	03/2019	237.51 -	12/2022 -	12/2022	0/0
488	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307]MoRTH,TRIPURA	01/2017	197.67 -	12/2022 -	12/2022	0/0
489	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA	03/2015	153.21 -	01/2017 -	-	0/0
490	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]MoRTH,KERALA	01/2014	255.75 348.00	09/2017 -	-	0/0
491	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MoRTH,MAHARASHTRA	10/2015	289.60 -	- -	-	0/0
492	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MoRTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-	0/0
493	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MoRTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-	0/0
494	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MoRTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-	0/0
495	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MoRTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-	0/0
496	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MoRTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-	0/0
497	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MoRTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
498	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]MoRTH,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-	0/0
499	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]MoRTH,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-	0/0
500	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]MoRTH,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 06/2018	-	0/0
501	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]MoRTH,NAGALAND	12/2010	1,296.00 -	02/2011 -	-	0/0
502	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MoRTH,TAMIL NADU	03/2015	258.97 -	08/2015 -	-	0/0
503	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MoRTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-	0/0
504	CONSTRUCTION OF PAVED SHOULDERS INCLUDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MoRTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-	0/0
505	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MoRTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-	0/0
506	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA	01/2015	225.81 -	- -	-	0/0
507	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-	0/0
508	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MoRTH,KARNATAKA	03/2015	159.12 -	11/2015 -	-	0/0
509	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]MoRTH,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	-	0/0
510	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]MoRTH,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	-	0/0
511	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]MoRTH,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	-	0/0
512	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MoRTH,KARNATAKA	01/1991	219.40 -	01/2018 -	-	0/0
513	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MoRTH,ODISHA	01/1991	218.63 -	10/2017 -	-	0/0
514	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH,BIHAR	01/1991	675.00 -	- -	-	0/0
515	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]MoRTH,PUNJAB	12/2015	766.36 -	- -	-	0/0
516	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]MoRTH,PUNJAB	11/2015	847.02 -	- -	-	0/0
517	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]MoRTH,ASSAM	11/2010	268.08 -	05/2017 -	-	0/0
518	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]MoRTH,MADHYA PRADESH	08/2015	257.80 -	- -	-	0/0
519	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]MoRTH,ASSAM	11/2010	470.20 -	02/2011 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
520	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MoRTH, WEST BENGAL	01/1991	322.00 -	03/2018 -	-	0/0
521	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MoRTH, BIHAR	01/1991	282.41 -	08/2016 -	-	0/0
522	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MoRTH, BIHAR	01/1991	358.22 -	10/2016 -	-	0/0
523	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]MoRTH, ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-	0/0
524	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MoRTH, ODISHA	01/1991	229.41 -	05/2018 -	-	0/0
525	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]MoRTH, ODISHA	07/2014	342.05 -	01/2017 -	-	0/0
526	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH, GOA	10/2015	936.40 -	- -	-	0/0
527	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]MoRTH, RAJASTHAN	09/2012	511.00 -	10/2013 -	-	0/0
528	WIDENING WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH, UTTAR PRADESH	05/2013	164.54 -	08/2015 -	-	0/0
529	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH, GOA	12/2015	773.98 -	- -	-	0/0
530	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MoRTH, GOA	12/2015	819.95 -	- -	-	0/0
531	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MoRTH, BIHAR	01/1991	478.35 -	- -	-	0/0
532	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]MoRTH, ODISHA	12/2011	159.39 -	11/2017 -	-	0/0
533	WIDENING STG. OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]MoRTH, PUNJAB	06/2015	892.17 -	- -	-	0/0
534	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH, ODISHA	12/2011	191.08 -	08/2015 -	-	0/0
535	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]MoRTH, BIHAR	01/1991	154.62 -	- -	-	0/0
536	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]MoRTH, BIHAR	01/1991	319.68 -	- -	-	0/0
537	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MoRTH, BIHAR	10/2013	278.39 -	08/2014 -	-	0/0
538	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MoRTH, BIHAR	11/2013	683.83 -	07/2016 -	-	0/0
539	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MoRTH, BIHAR	02/2014	665.50 -	07/2016 -	-	0/0
540	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MoRTH, BIHAR	02/2016	178.85 -	05/2016 -	-	0/0
541	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MoRTH, BIHAR	02/2016	369.77 -	06/2016 -	-	0/0
542	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MoRTH, BIHAR	02/2016	553.30 -	05/2016 -	-	0/0
543	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH, BIHAR	01/2014	1,408.85 -	10/2016 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
544	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPR - [N24000580]MoRTH,BIHAR	03/2015	206.80 -	07/2016 -	-	0/0
545	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MoRTH,BIHAR	08/2015	288.24 -	11/2015 -	-	0/0
546	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH,MAHARASHTRA	03/2016	1,142.62 -	- -	-	0/0
547	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH,MAHARASHTRA	03/2016	1,101.58 -	- -	-	0/0
548	REHABILITATION OF 4-LANE 5.575 KM LONG, 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH,BIHAR	08/2016	1,742.01 -	12/2016 -	-	0/0
549	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH,ODISHA	03/2014	191.50 192.00	05/2016 -	-	0/0
550	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY W - [N24000640]MoRTH,ODISHA	01/2015	326.63 327.00	04/2018 -	-	0/0
551	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MoRTH,ODISHA	02/2015	239.91 240.00	10/2017 -	-	0/0
552	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MoRTH,ODISHA	07/2014	342.05 342.00	01/2017 -	-	0/0
553	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH,ODISHA	08/2013	171.96 172.00	06/2016 -	-	0/0
554	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MoRTH,ODISHA	06/2016	157.30 157.00	06/2018 -	-	0/0
555	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH,UTTARAKHAND	12/2017	257.34 -	12/2019 -	-	0/0
556	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH,UTTARAKHAND	12/2017	200.34 -	12/2019 -	-	0/0
557	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MoRTH,UTTARAKHAND	12/2017	248.22 -	12/2019 -	-	0/0
558	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MoRTH,UTTARAKHAND	06/2017	282.08 -	06/2019 -	-	0/0
559	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING TWO LANE TO 2-LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH,UTTARAKHAND	11/2017	232.81 -	11/2019 -	-	0/0
560	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH,UTTARAKHAND	11/2017	283.51 -	11/2019 -	-	0/0
561	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH,UTTARAKHAND	11/2017	266.52 -	11/2019 -	-	0/0
562	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MoRTH,UTTARAKHAND	02/2018	418.88 -	02/2020 -	-	0/0
563	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MoRTH,UTTARAKHAND	02/2018	293.68 -	- -	-	0/0
564	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MoRTH,UTTARAKHAND	05/2018	248.00 -	05/2020 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
565	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH,UTTARAKHAND	03/2018	460.73 -	- -	-	0/0
566	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MoRTH,A & N ISLANDS	11/2017	237.80 -	11/2019 -	-	0/0
567	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH,A & N ISLANDS	11/2017	257.34 -	11/2019 -	-	0/0
568	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O - [N24000871]MoRTH,WEST BENGAL	08/2014	600.87 720.97	11/2017 -	-	0/0
569	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH	03/2018	166.21 -	08/2018 -	-	0/0
570	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873]MoRTH,WEST BENGAL	08/2014	823.20 937.76	11/2017 -	-	0/0
571	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879]MoRTH,WEST BENGAL	03/2017	202.69 202.69	11/2019 -	-	0/0
572	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906]MoRTH,PUNJAB	03/2018	173.24 -	06/2020 -	-	0/0
573	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]MoRTH,PUNJAB	03/2018	293.10 -	08/2020 -	-	0/0
574	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) - [N24000908]MoRTH,HARYANA	01/2017	276.01 -	03/2019 -	-	0/0
575	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26. - [N24000911]MoRTH,ODISHA	03/2016	165.06 -	12/2016 -	-	0/0
576	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MoRTH,ODISHA	08/2016	287.70 -	02/2017 -	-	0/0
577	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH,ODISHA	09/2016	295.67 -	02/2017 -	-	0/0
578	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH,ODISHA	12/2016	223.50 -	08/2018 -	-	0/0
579	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH,ODISHA	12/2016	206.88 -	04/2018 -	-	0/0
580	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH,ODISHA	03/2018	214.23 -	08/2018 -	-	0/0
581	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH,ODISHA	03/2018	199.16 -	08/2018 -	-	0/0
582	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927]MoRTH,PUNJAB	03/2018	293.64 -	08/2020 -	-	0/0
583	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]MoRTH,PUNJAB	03/2018	293.64 -	08/2020 -	-	0/0
584	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR	09/2018	1,478.40 -	- -	-	0/0
585	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 - [N24000962]MoRTH,MADHYA PRADESH	09/2016	178.23 -	09/2018 -	-	0/0
586	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA	10/2016	298.32 -	02/2019 -	-	0/0
587	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA	10/2016	248.83 -	03/2019 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
588	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037 OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH, TELANGANA	01/2017	244.54 -	05/2019 -	-	0/0
589	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]MoRTH, TELANGANA	01/2017	196.52 -	10/2019 -	-	0/0
590	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]MoRTH, TELANGANA	01/2017	283.00 -	12/2019 -	-	0/0
591	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNAGUDA-RAVULAPALLY SECT - [N24000985]MoRTH, TELANGANA	01/2017	359.27 -	05/2019 -	-	0/0
592	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH, TELANGANA	01/2017	300.00 -	05/2019 -	-	0/0
593	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]MoRTH, TELANGANA	01/2018	283.15 -	05/2020 -	-	0/0
594	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]MoRTH, TELANGANA	01/2018	230.03 -	12/2019 -	-	0/0
595	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]MoRTH, TELANGANA	02/2018	206.13 -	06/2020 -	-	0/0
596	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH, TELANGANA	02/2018	294.13 -	11/2019 -	-	0/0
597	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH, TELANGANA	02/2018	220.28 -	11/2019 -	-	0/0
598	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]MoRTH, TELANGANA	02/2018	426.52 -	04/2020 -	-	0/0
599	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]MoRTH, TELANGANA	03/2018	322.81 -	09/2020 -	-	0/0
600	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]MoRTH, TELANGANA	03/2018	626.76 -	07/2020 -	-	0/0
601	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH, TELANGANA	01/2017	605.08 -	10/2019 -	-	0/0
602	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL - MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH, TELANGANA	03/2018	192.67 -	07/2019 -	-	0/0
603	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH, TELANGANA	01/2019	193.19 -	-	-	0/0
604	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C - [N24000999]MoRTH, BIHAR	11/2016	230.34 -	10/2019 -	-	0/0
605	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH, BIHAR	03/2018	153.24 -	-	-	0/0
606	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]MoRTH, BIHAR	05/2014	199.98 -	08/2016 -	-	0/0
607	KHAMGAON TO SHEGAON - [N24001009]MoRTH, MAHARASHTRA	02/2017	203.21 203.00	05/2019 -	-	0/0
608	DIGRAS DARWAH KARANJA - [N24001013]MoRTH, MAHARASHTRA	01/2017	391.06 391.00	06/2019 -	-	0/0
609	NANDGAON TO MORSHI - [N24001014]MoRTH, MAHARASHTRA	01/2017	385.87 386.00	06/2019 -	-	0/0
610	MORSHI TO ACHALPUR - [N24001015]MoRTH, MAHARASHTRA	01/2017	341.16 341.00	06/2019 -	-	0/0
611	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH, MAHARASHTRA	01/2017	471.61 472.00	06/2019 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
612	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA	01/2017	392.83 393.00	06/2019 -	-	0/0
613	MAJALGAON TO KAIJ - [N24001036]MoRTH,MAHARASHTRA	01/2017	413.99 -	07/2019 -	-	0/0
614	BHADGAON TO CHALISGAON - [N24001047]MoRTH,MAHARASHTRA	01/2018	259.55 260.00	11/2019 -	-	0/0
615	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA	01/2017	232.77 -	07/2019 -	-	0/0
616	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA	02/2017	422.02 422.00	07/2019 -	-	0/0
617	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA	09/2018	301.38 301.00	08/2020 -	-	0/0
618	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA	03/2018	249.29 -	12/2019 -	-	0/0
619	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA	03/2018	219.91 -	12/2019 -	-	0/0
620	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA	03/2018	228.31 -	12/2019 -	-	0/0
621	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA	03/2018	256.15 -	12/2019 -	-	0/0
622	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA	03/2018	223.46 -	12/2019 -	-	0/0
623	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA	03/2018	177.84 177.00	12/2019 -	-	0/0
624	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA	12/2017	309.94 310.00	12/2019 -	-	0/0
625	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA	12/2017	244.04 244.00	03/2019 -	-	0/0
626	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA	01/2017	388.44 -	- -	-	0/0
627	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA	01/2018	264.41 264.00	03/2019 -	-	0/0
628	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA	02/2017	406.51 -	06/2019 -	-	0/0
629	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND	08/2016	234.88 -	12/2017 -	-	0/0
630	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	-	0/0
631	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA - [N24001139]MoRTH,UTTAR PRADESH	10/2016	218.94 219.00	03/2020 -	-	0/0
632	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]MoRTH,UTTAR PRADESH	11/2016	215.16 215.00	09/2019 -	-	0/0
633	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO - [N24001143]MoRTH,UTTAR PRADESH	10/2016	176.94 177.00	10/2018 -	-	0/0
634	REHABILITATION AND UPGRADATION OF ALLAHABAD - MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2- [N24001147]MoRTH,UTTAR PRADESH	10/2016	239.63 -	02/2019 -	-	0/0
635	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148]MoRTH,UTTAR PRADESH	03/2016	599.34 -	01/2020 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
636	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA	02/2018	355.99 -	12/2019 -	-	0/0
637	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM - [N24001153]MoRTH,ASSAM	11/2010	197.37 -	02/2014 -	-	0/0
638	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT - [N24001154]MoRTH,KARNATAKA	08/2016	367.44 -	01/2017 -	-	0/0
639	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT - [N24001155]MoRTH,KARNATAKA	08/2016	175.20 -	01/2017 -	-	0/0
640	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS - PA - [N24001156]MoRTH,KARNATAKA	01/2017	166.67 -	09/2017 -	-	0/0
641	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA	08/2016	175.50 -	02/2017 -	-	0/0
642	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA	03/2018	159.97 -	06/2019 -	-	0/0
643	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]MoRTH,KARNATAKA	01/2018	159.70 -	07/2018 -	-	0/0
644	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA	09/2017	191.60 -	10/2018 -	-	0/0
645	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- [N24001161]MoRTH,KARNATAKA	12/2017	297.30 -	01/2019 -	-	0/0
646	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA	03/2018	325.86 -	10/2018 -	-	0/0
647	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]MoRTH,KARNATAKA	08/2016	329.01 -	02/2017 -	-	0/0
648	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA	10/2016	396.96 -	03/2017 -	-	0/0
649	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA	11/2016	314.90 -	03/2017 -	-	0/0
650	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA	03/2015	159.12 -	01/2016 -	-	0/0
651	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776) - [N24001167]MoRTH,KARNATAKA	03/2015	165.67 -	01/2016 -	-	0/0
652	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA	05/2018	171.60 -	05/2018 -	-	0/0
653	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM. - [N24001170]MoRTH,KARNATAKA	01/2014	471.16 -	08/2014 -	-	0/0
654	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA	01/2017	291.49 -	08/2017 -	-	0/0
655	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND	11/2016	336.25 369.96	09/2019 11/2020	-	0/0
656	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S - [N24001183]MoRTH,ANDHRA PRADESH	07/2014	251.55 -	02/2015 -	-	0/0
657	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR	02/2019	2,926.42 -	- -	-	0/0
658	REHABILITATION AND UPGRADATION OF BARAICH -SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA - [N24001202]MoRTH,UTTAR PRADESH	03/2016	388.83 -	12/2019 -	-	0/0
659	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH,UTTAR PRADESH	03/2018	306.59 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
660	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH,UTTAR PRADESH	11/2018	281.45 -	- -	-	0/0
661	WIDENING OF SL TO 2 L KM. 107-184.80 SUKUMA TO KONTA ON NH 221 - [N24001223]MoRTH,CHANDIGARH	03/2010	179.89 271.00	03/2013 05/2019	-	0/0
662	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1 - [N24001225]MoRTH,CHANDIGARH	12/2010	169.26 299.00	01/2019 -	-	0/0
663	WIDENING TO 4 LANE / 4 LANE WITH PAVED SHOULDERS WITH STRENGTHENING OF EXISTING CARRIAGEWAY IN KM 0/ - [N24001237]MoRTH,TAMIL NADU	01/2016	162.72 -	09/2016 -	-	0/0
664	CONSTRUCTION OF FLYOVER FROM KM 604/252 TO 607/060 (MARTHANDAM JUNCTION) AND FROM KM 630/116 TO 631/ - [N24001238]MoRTH,TAMIL NADU	05/2016	307.70 -	01/2017 -	-	0/0
665	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM - [N24001239]MoRTH,TAMIL NADU	03/2018	240.38 -	06/2019 -	-	0/0
666	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W - [N24001243]MoRTH,ASSAM	03/2020	166.94 -	12/2020 -	-	0/0
667	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1) - [N24001289]MoRTH,ARUNACHAL PRADESH	03/2019	403.68 -	02/2020 -	-	0/0
668	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2 - [N24001290]MoRTH,ARUNACHAL PRADESH	03/2019	342.55 -	02/2020 -	-	0/0
669	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE - [N24001291]MoRTH,ARUNACHAL PRADESH	03/2019	421.48 -	11/2020 -	-	0/0
670	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE - [N24001292]MoRTH,ARUNACHAL PRADESH	03/2019	543.05 -	11/2020 -	-	0/0
671	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE - [N24001293]MoRTH,ARUNACHAL PRADESH	03/2019	486.70 -	10/2020 -	-	0/0
672	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE - [N24001294]MoRTH,ARUNACHAL PRADESH	03/2019	560.39 -	02/2020 -	-	0/0
673	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE - [N24001295]MoRTH,ARUNACHAL PRADESH	03/2019	347.78 -	09/2020 -	-	0/0
674	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG - [N24001296]MoRTH,ARUNACHAL PRADESH	03/2019	394.27 -	10/2020 -	-	0/0
675	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE - [N24001297]MoRTH,ARUNACHAL PRADESH	03/2019	450.65 -	11/2020 -	-	0/0
676	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 - [N24000895]MoRTH,MADHYA PRADESH	09/2016	287.34 -	01/2019 09/2020	11/2020	0/0
677	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH,ARUNACHAL PRADESH	09/2011	1,979.00 -	- 03/2020	-	0/0
<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
678	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND	03/2018	339.57 -	09/2018 -	07/2022	0/0
679	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND	03/2018	500.09 336.49	09/2018 -	11/2022	0/0
680	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM	04/2017	519.09 -	09/2019 -	04/2023	0/0
681	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM	04/2017	473.18 -	09/2019 -	04/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
682	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM	04/2017	537.82 -	09/2019 -	04/2023	0/0
683	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM	04/2017	642.96 -	09/2019 -	06/2023	0/0
684	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM	04/2017	518.53 -	09/2019 -	06/2023	0/0
685	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM	04/2017	640.07 -	09/2019 -	07/2023	0/0
686	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM	04/2017	428.11 -	09/2019 -	09/2023	0/0
687	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM	04/2017	404.29 -	09/2019 -	04/2024	0/0
688	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR	03/2018	253.44 -	07/2019 -	-	0/0
689	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH	12/2016	200.44 -	- -	-	0/0
690	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH	03/2017	1,718.59 -	- -	-	0/0
691	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH	09/2016	568.92 -	- -	-	0/0
692	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH	12/2016	188.78 -	- -	-	0/0
693	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8 - [N24001184]NHIDCL,DELHI	07/2017	269.69 -	09/2019 -	-	0/0
694	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL,ASSAM	03/2017	1,049.51 -	- -	-	0/0
National Highways Authority Of India						
695	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- -	01/2020	0/0
696	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	- -	01/2021	0/0
697	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	03/2019 -	02/2021	0/0
698	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	07/2016 -	02/2021	0/0
699	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 -	03/2021	0/0
700	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	03/2021	0/0
701	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	06/2018 -	03/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
702	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	08/2019 -	03/2021	0/0
703	4-LANNING OF KODEBAD-DHANTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	03/2019 -	03/2021	0/0
704	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA	03/2018	806.11 -	- -	04/2021	0/0
705	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	- -	08/2020	0/0
706	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	10/2017 -	11/2020	0/0
707	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	04/2018 -	12/2020	0/0
708	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	06/2015	0/0
709	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- 06/2015	06/2015	0/0
710	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	07/2018	0/0
711	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 -	06/2019	0/0
712	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	04/2010 -	07/2019	0/0
713	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 -	09/2019	0/0
714	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	06/2019 -	09/2019	0/0
715	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 627.93	01/2016 01/2020	01/2020	0/0
716	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 686.13	- -	05/2020	0/0
717	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 679.94	- -	05/2020	0/0
718	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	06/2020	0/0
719	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 -	08/2020	0/0
720	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	09/2020	0/0
721	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN	02/2018	1,103.88 -	- -	09/2020	0/0
722	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	10/2020	0/0
723	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	10/2020	0/0
724	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 -	- -	10/2020	0/0
725	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	03/2019 -	11/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
726	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 469.31	01/2014 12/2020	12/2020	0/0
727	2-LANING WITH PAVED SHOULDERS OF RAIBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 417.68	01/2016 12/2020	12/2020	0/0
728	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	08/2016 -	12/2020	0/0
729	FOUR LANING OF RAMBAN - BANIHAI SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	12/2020	0/0
730	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20 -	04/2020 -	12/2020	0/0
731	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA	03/2018	1,484.30 -	- 06/2021	12/2020	0/0
732	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 585.00	11/2013 12/2020	01/2021	0/0
733	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT	02/2018	1,052.21 -	- -	01/2021	0/0
734	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	04/2008 -	02/2021	0/0
735	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	07/2018 -	02/2021	0/0
736	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH	03/2018	565.09 -	- -	02/2021	0/0
737	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	03/2021	0/0
738	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	11/2018 07/2019	03/2021	0/0
739	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	08/2018 -	03/2021	0/0
740	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	- -	03/2021	0/0
741	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	- -	03/2021	0/0
742	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH	03/2018	1,029.96 -	- -	03/2021	0/0
743	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	- -	04/2021	0/0
744	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	- -	05/2021	0/0
745	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA	03/2017	639.79 -	03/2020 05/2021	05/2021	0/0
746	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	03/2020 -	05/2021	0/0
747	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	09/2017 -	05/2021	0/0
748	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH	03/2018	478.74 -	- -	05/2021	0/0
749	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	05/2018 06/2021	06/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
750	REHABILITATION AND UPGRADATION TO FOUR LANE OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	- -	06/2021	0/0
751	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	03/2020 -	06/2021	0/0
752	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	07/2017 -	06/2021	0/0
753	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	- -	06/2021	0/0
754	REHABILITATION AND UPGRADATION OF FOUR LANE OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	- -	06/2021	0/0
755	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	- -	06/2021	0/0
756	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	- -	06/2021	0/0
757	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	- -	06/2021	0/0
758	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	- -	06/2021	0/0
759	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	- -	06/2021	0/0
760	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT	03/2018	2,702.05 -	- -	06/2021	0/0
761	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	- -	07/2021	0/0
762	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN	04/2017	894.00 -	04/2020 -	07/2021	0/0
763	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	- -	07/2021	0/0
764	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI,WEST BENGAL	03/2018	1,261.98 -	- -	07/2021	0/0
765	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB	02/2018	261.76 -	- -	07/2021	0/0
766	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64 -	- -	07/2021	0/0
767	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA	03/2018	634.70 -	- -	07/2021	0/0
768	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA	03/2018	795.50 -	- -	07/2021	0/0
769	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 -	- -	07/2021	0/0
770	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	08/2021	0/0
771	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	- -	08/2021	0/0
772	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26 -	- -	08/2021	0/0
773	FOUR LANING OF CHETTICKULAM TO NATHAM SECTION OF NH-785 FROM CHETTICKULAM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35 -	- -	08/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
774	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21 -	- 02/2021	08/2021	0/0
775	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	04/2019 -	09/2021	0/0
776	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	- -	09/2021	0/0
777	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	06/2020 -	09/2021	0/0
778	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 -	- -	09/2021	0/0
779	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 -	- -	10/2021	0/0
780	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 -	- -	11/2021	0/0
781	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	07/2019 06/2021	12/2021	0/0
782	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	07/2019 06/2021	12/2021	0/0
783	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	03/2019 01/2021	12/2021	0/0
784	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 932.23	03/2020 -	12/2021	0/0
785	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	03/2020 -	12/2021	0/0
786	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	- -	12/2021	0/0
787	FOUR LANING OF MADURAI- CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICKULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	- -	12/2021	0/0
788	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA - [N24001302]NHAI,TAMIL NADU	07/2020	3,426.00 -	12/2021 -	12/2021	0/0
789	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	01/2022	0/0
790	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU	03/2018	1,016.92 -	- -	01/2022	0/0
791	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	08/2017 -	02/2022	0/0
792	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53 -	- 08/2021	02/2022	0/0
793	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	03/2019 12/2021	03/2022	0/0
794	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	03/2019 03/2022	03/2022	0/0
795	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	- -	03/2022	0/0
796	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43 -	- -	03/2022	0/0
797	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	08/2017 -	07/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
798	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	09/2017 -	07/2022	0/0
799	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014 -	12/2022	0/0
800	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN - [N24001306]NHAI,UTTAR PRADESH	10/2020	724.60 -	03/2023 -	03/2023	0/0
801	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	-	0/0
802	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	-	0/0
803	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	-	0/0
804	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-	0/0
805	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	-	0/0
806	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-	0/0
807	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	-	0/0
808	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	-	0/0
809	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	-	0/0
810	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-	0/0
811	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-	0/0
812	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-	0/0
813	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-	0/0
814	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	-	0/0
815	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-	0/0
816	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	-	0/0
817	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	-	0/0
818	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-	0/0
819	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	-	0/0
820	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	-	0/0
821	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
822	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	10/2013 -	-	0/0
823	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	06/2015 -	-	0/0
824	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-	0/0
825	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	-	0/0
826	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	09/2016 -	-	0/0
827	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 -	-	0/0
828	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	11/2017 -	-	0/0
829	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	12/2017 -	-	0/0
830	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 -	05/2017 -	-	0/0
831	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	-	0/0
832	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	-	0/0
833	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 -	-	0/0
834	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	05/2019 -	-	0/0
835	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI,WEST BENGAL	10/2015	361.15 -	- -	-	0/0
836	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	05/2019 -	-	0/0
837	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	06/2016 -	-	0/0
838	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	04/2018 -	-	0/0
839	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 -	07/2018 -	-	0/0
840	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	01/2019 -	-	0/0
841	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	07/2017 -	-	0/0
842	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	-	0/0
843	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-	0/0
844	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 -	06/2018 -	-	0/0
845	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
846	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	-	0/0
847	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 -	03/2018 -	-	0/0
848	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	04/2019 -	-	0/0
849	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	-	0/0
850	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	08/2018 -	-	0/0
851	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 -	06/2018 -	-	0/0
852	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	-	0/0
853	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	-	0/0
854	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	05/2018 -	-	0/0
855	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	-	0/0
856	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 -	07/2018 -	-	0/0
857	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 -	06/2018 -	-	0/0
858	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	04/2018 -	-	0/0
859	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 -	12/2017 -	-	0/0
860	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	- -	-	0/0
861	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 -	01/2018 -	-	0/0
862	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	-	0/0
863	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	- -	-	0/0
864	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	05/2018 -	-	0/0
865	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	- -	-	0/0
866	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-	0/0
867	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 -	06/2019 -	-	0/0
868	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR-HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 -	07/2018 -	-	0/0
869	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	04/2019 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
870	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	11/2018 -	-	0/0
871	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	02/2019 -	-	0/0
872	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-	0/0
873	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 -	03/2019 -	-	0/0
874	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-	0/0
875	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	04/2019 -	-	0/0
876	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI,WEST BENGAL	03/2016	229.37 -	11/2018 -	-	0/0
877	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	04/2019 -	-	0/0
878	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	- -	-	0/0
879	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	- -	-	0/0
880	4-LANNING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	-	0/0
881	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	- -	-	0/0
882	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	- -	-	0/0
883	SIX-LANNING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	-	0/0
884	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	06/2019 -	-	0/0
885	BALANCE WORK OF 4 LANING OF GORAKHPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	-	0/0
886	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 -	- -	-	0/0
887	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	-	0/0
888	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	10/2018 -	-	0/0
889	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS- WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	- -	-	0/0
890	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	04/2019 -	-	0/0
891	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 -	09/2019 -	-	0/0
892	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 -	- -	-	0/0
893	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
894	FOUR LANNING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	08/2018 -	-	0/0
895	CONSTRUCTION OF FOUR LANNING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	05/2019 -	-	0/0
896	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-	0/0
897	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 -	08/2018 -	-	0/0
898	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 -	08/2019 -	-	0/0
899	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA	09/2016	1,004.67 -	05/2019 -	-	0/0
900	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	- -	-	0/0
901	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-	0/0
902	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	-	0/0
903	4 LANNING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	07/2018 -	-	0/0
904	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-	0/0
905	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	- -	-	0/0
906	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	05/2019 -	-	0/0
907	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 -	02/2020 -	-	0/0
908	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA	03/2017	247.02 -	03/2020 -	-	0/0
909	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA	03/2017	744.64 -	03/2020 -	-	0/0
910	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	-	0/0
911	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA	03/2017	296.19 -	03/2020 -	-	0/0
912	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	03/2020 -	-	0/0
913	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR	03/2017	672.89 -	03/2020 -	-	0/0
914	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	-	0/0
915	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH	03/2017	2,064.99 -	03/2020 -	-	0/0
916	SIX LANNING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	03/2020 -	-	0/0
917	SIX LANNING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	03/2020 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
918	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	-	0/0
919	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	-	0/0
920	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	- -	-	0/0
921	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	- -	-	0/0
922	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	- -	-	0/0
923	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	- -	-	0/0
924	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-	0/0
925	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- -	-	0/0
926	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-	0/0
927	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 -	- -	-	0/0
928	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-	0/0
929	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-	0/0
930	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-	0/0
931	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 -	- -	-	0/0
932	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA	03/2017	4,429.00 -	03/2017 -	-	0/0
933	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA	02/2018	486.78 -	- -	-	0/0
934	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 -	- -	-	0/0
935	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 -	- -	-	0/0
936	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 -	- -	-	0/0
937	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 -	- -	-	0/0
938	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH	03/2018	925.40 -	- -	-	0/0
939	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN	02/2018	741.86 -	- -	-	0/0
940	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN	02/2018	716.76 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
941	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	-	0/0
942	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 -	- -	-	0/0
943	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH	03/2018	1,025.80 -	- -	-	0/0
944	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH	03/2018	1,115.28 -	- -	-	0/0
945	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K - [N24000804]NHAI,TELANGANA	03/2018	802.65 -	- -	-	0/0
946	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 -	- -	-	0/0
947	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-	0/0
948	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	- -	-	0/0
949	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	- -	-	0/0
950	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA	03/2018	950.63 -	- -	-	0/0
951	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA	03/2018	857.62 -	- -	-	0/0
952	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHTRA - [N24000825]NHAI,TELANGANA	03/2018	828.29 -	- -	-	0/0
953	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU	03/2018	633.55 -	- -	-	0/0
954	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU	03/2018	2,065.96 -	- -	-	0/0
955	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE	03/2018	1,294.47 -	- -	-	0/0
956	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE	03/2018	998.70 -	- -	-	0/0
957	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT	03/2018	1,161.39 -	- -	-	0/0
958	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA	03/2018	275.12 -	- -	-	0/0
959	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTI - [N24000837]NHAI,HARYANA	03/2018	307.79 -	- -	-	0/0
960	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE - DANTOUR-JA - [N24000838]NHAI,RAJASTHAN	03/2018	874.25 -	- -	-	0/0
961	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN	03/2018	1,158.35 -	- -	-	0/0
962	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB	03/2018	199.90 -	- -	-	0/0
963	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB	03/2018	196.05 -	- -	-	0/0
964	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA	03/2018	198.05 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
965	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA	03/2018	181.78 -	- -	-	0/0
966	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA	03/2018	551.58 -	- -	-	0/0
967	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA	03/2018	642.13 -	- -	-	0/0
968	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 -	- -	-	0/0
969	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - [N24001185]NHAI,UTTAR PRADESH	11/2017	2,159.00 -	01/2019 -	-	0/0
970	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI,HARYANA	01/2019	1,051.91 -	- -	-	0/0
971	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI,HARYANA	01/2019	1,120.06 -	- -	-	0/0
972	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA	01/2019	1,137.42 -	- -	-	0/0
973	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA	01/2019	1,033.19 -	- -	-	0/0
974	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA	01/2019	1,243.45 -	- -	-	0/0
975	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA	01/2019	889.36 -	- -	-	0/0
976	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA	01/2019	1,018.79 -	- -	-	0/0
977	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA	01/2019	996.65 -	- -	-	0/0
978	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105 - [N24001298]NHAI,ANDHRA PRADESH	09/2018	597.67 -	01/2020 -	-	0/0
979	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN - [N24001299]NHAI,ANDHRA PRADESH	09/2018	617.41 -	02/2019 -	-	0/0
980	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300]NHAI,ANDHRA PRADESH	11/2019	1,226.88 -	02/2021 -	-	0/0
981	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - [N24001301]NHAI,ANDHRA PRADESH	11/2019	1,601.10 -	02/2021 -	-	0/0
982	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT - [N24001303]NHAI,BIHAR	10/2013	649.90 -	12/2020 -	-	0/0
983	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE - [N24001304]NHAI,BIHAR	10/2013	446.97 -	11/2020 -	-	0/0
984	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA - [N24001305]NHAI,BIHAR	10/2013	464.09 -	11/2020 -	-	0/0
985	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	-	0/0
	<u>SHIPPING AND PORTS</u>					
	<u>Inland Waterways Authority Of India</u>					
986	JAL MARG VIKAS PROJECT - [N25000072]IWAI,MULTI STATE	01/2018	5,369.18 -	03/2023 -	03/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	<u>TELECOMMUNICATIONS</u>					
	<u>Bharat Sanchar Nigam Limited</u>					
987	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114]BSNL,MULTI STATE	03/2020	431.16 431.00	06/2021 -	11/2021	0/0
	<u>Central Public Works Department</u>					
988	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI	10/2016	248.20 -	03/2018 -	06/2021	0/0
	<u>Department Of Telecommunication</u>					
989	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	07/2015 -	07/2021	0/0
	<u>URBAN DEVELOPMENT</u>					
	<u>Ahmedabad Metro Rail</u>					
990	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT	11/2014	10,773.00 -	12/2018 -	08/2022	0/0
991	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137]MEGA,GUJARAT	03/2019	5,384.17 -	03/2024 -	03/2024	0/0
992	SURAT METRO RAIL PROJECT - [N28000138]MEGA,GUJARAT	03/2019	12,020.32 -	03/2024 -	03/2024	0/0
	<u>Central Public Works Department</u>					
993	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00 -	03/2021 07/2021	07/2021	0/0
994	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 -	08/2020 -	03/2022	0/0
995	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]CPWD,DELHI	10/2016	1,128.00 -	03/2022 -	03/2022	0/0
996	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I - [N28000128]CPWD,DELHI	10/2016	1,180.00 -	07/2021 -	12/2024	0/0
997	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	12/2015 -	-	0/0
998	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	12/2013 -	-	0/0
999	C/O STEEL STRUCTURE BUILDINGS USING PRE-ENGINEERED TECHNOLOGY AT AFRICA AVENUE AND KG MARG - [N28000143]CPWD,DELHI	02/2020	532.00 -	11/2020 -	-	0/0
1000	CONSTRUCTION 729 QUARTERS (TYPE II-180, TYPE III-364, TYPE IV-112,TYPE V-68, TYPE-VI-5), SHOPS,CO - [N28000149]CPWD,CHHATISGARH	05/2019	299.97 -	09/2020 -	-	0/0
	<u>Delhi Metro Rail Corporation</u>					
1001	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	03/2016 -	09/2021	0/0
1002	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136]DMRC,DELHI	05/2017	565.00 -	12/2020 -	09/2021	0/0
1003	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS - [N28000135]DMRC,DELHI	07/2019	24,948.65 -	03/2025 -	03/2025	0/0
	<u>Kochi Metro Rail Corporation Ltd</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
1004	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	07/2017 -	09/2020	0/0
	<u>Lucknow Metro Rail Corporation Limited</u>					
1005	KANPUR METRO RAIL PROJECT - [N28000144]LMRCL,UTTAR PRADESH	05/2019	11,076.48 -	03/2024 -	03/2024	0/0
1006	AGRA METRO RAIL PROJECT - [N28000145]LMRCL,UTTAR PRADESH	05/2019	8,379.62 -	03/2024 -	03/2024	0/0
1007	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	-	0/0
	<u>Maharashtra Metro Rail Corporation Ltd.</u>					
1008	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA	12/2016	11,420.00 11,420.00	11/2021 -	11/2021	0/0
	<u>Mumbai Metro Rail Corporation Ltd</u>					
1009	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	03/2023	0/0
	<u>Madhya Pradesh Metro Rail Co Limited</u>					
1010	BHOPAL METRO RAIL - [N28000124]MPMRCL,MADHYA PRADESH	11/2018	6,941.40 -	02/2023 -	02/2023	0/0
1011	INDORE METRO RAIL - [N28000125]MPMRCL,MADHYA PRADESH	11/2018	7,500.80 -	02/2023 -	02/2023	0/0
	<u>Nagpur Metro Rail Corporation Ltd</u>					
1012	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	-	0/0
	<u>National Capital Region Transport Corp</u>					
1013	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134]NCRTC,MULTI STATE	03/2019	30,274.00 -	06/2025 -	06/2025	0/0
	<u>Patna Metro Rail Corporation</u>					
1014	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]PATNA METRO RAI,BIHAR	02/2019	13,365.77 -	06/2024 -	06/2024	0/0
	<u>WATER RESOURCES</u>					
	<u>Brahmaputra Board</u>					
1015	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPPB,MAHARASHTRA	03/2017	233.57 -	12/2019 -	12/2021	0/0
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>					
1016	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]BUIDCO,BIHAR	12/2014	225.77 -	03/2020 -	03/2021	0/0
1017	I AND D AND STP AT CHAPPRRA - [N30000028]BUIDCO,BIHAR	11/2018	236.15 -	12/2020 06/2021	04/2021	0/0
1018	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]BUIDCO,BIHAR	05/2017	356.37 -	04/2021 -	04/2021	0/0
1019	SEWERAGE SCHEME AT PAHARI ZONE IVA S PATNA - [N30000041]BUIDCO,BIHAR	05/2017	184.86 -	05/2021 -	05/2021	0/0
1020	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]BUIDCO,BIHAR	03/2017	277.42 -	05/2021 -	05/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
1021	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR - [N30000038]BUIDCO,BIHAR	04/2015	184.93 -	04/2020 -	06/2021	0/0
1022	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026]BUIDCO,BIHAR	03/2018	230.06 -	07/2021 -	07/2021	0/0
1023	SEWER NETWORKS, SPS AND STP, MUNGER - [N30000036]BUIDCO,BIHAR	03/2018	294.02 -	10/2021 -	10/2021	0/0
1024	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]BUIDCO,BIHAR	03/2018	305.19 -	08/2021 -	12/2021	0/0
1025	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]BUIDCO,BIHAR	08/2017	578.89 -	06/2022 -	06/2022	0/0
1026	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA - [N30000051]BUIDCO,BIHAR	08/2017	824.00 -	06/2022 -	06/2022	0/0
1027	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO,BIHAR	10/2017	254.13 -	09/2020 -	-	0/0
1028	SAIDPUR SEWER NETWORK PATNA - [N30000039]BUIDCO,BIHAR	04/2015	268.63 -	01/2021 -	-	0/0
1029	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]BUIDCO,BIHAR	05/2017	191.62 -	11/2020 03/2021	-	0/0
<u>Delhi Jal Board</u>						
1030	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI - [N30000017]DJB,DELHI	12/2018	515.07 -	01/2021 -	06/2021	0/0
1031	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014]DJB,DELHI	03/2017	665.78 -	12/2022 -	12/2022	0/0
1032	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015]DJB,DELHI	05/2016	211.79 -	12/2021 -	12/2022	0/0
1033	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]DJB,DELHI	05/2016	239.11 -	02/2022 -	12/2022	0/0
1034	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018]DJB,DELHI	05/2017	344.81 -	05/2020 -	-	0/0
<u>Kolkata Metropolitan Development Authority</u>						
1035	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]KMDA, WEST BENGAL	12/2014	272.32 -	04/2020 -	03/2021	0/0
1036	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046]KMDA, WEST BENGAL	02/2014	274.76 -	12/2019 05/2021	05/2021	0/0
1037	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]KMDA, WEST BENGAL	08/2017	185.22 -	12/2021 -	12/2021	0/0
1038	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048]KMDA, WEST BENGAL	01/2018	172.10 -	12/2021 -	12/2021	0/0
1039	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]KMDA, WEST BENGAL	10/2017	164.93 -	12/2021 -	12/2021	0/0
1040	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]KMDA, WEST BENGAL	01/2019	384.96 -	04/2022 -	04/2022	0/0
1041	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPUR - [N30000030]KMDA, WEST BENGAL	03/2019	287.53 -	04/2022 -	04/2022	0/0
1042	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]KMDA, WEST BENGAL	12/2018	234.31 -	04/2022 -	04/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
1043	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]KMDA, WEST BENGAL	05/2018	198.43 224.69	02/2022 -	06/2022	0/0
1044	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033]KMDA, WEST BENGAL	03/2018	165.16 -	06/2022 -	06/2022	0/0
1045	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA - [N30000034]KMDA, WEST BENGAL	08/2017	307.12 -	09/2022 -	09/2022	0/0
1046	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH - [N30000042]KMDA, WEST BENGAL	05/2018	160.00 154.73	02/2022 -	10/2022	0/0
	<u>Uttar Pradesh Jal Nigam</u>					
1047	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020]UP JalNigam, UTTAR PRADESH	02/2011	279.91 330.05	12/2019 -	01/2021	0/0
1048	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA - [N30000011]UP JalNigam, UTTAR PRADESH	02/2017	161.31 -	11/2019 -	03/2021	0/0
1049	MATHURA SEWERAGE SCHEME - [N30000019]UP JalNigam, UTTAR PRADESH	12/2017	460.45 -	12/2020 -	05/2021	0/0
1050	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH - [N30000013]UP JalNigam, UTTAR PRADESH	03/2019	271.39 -	08/2021 -	08/2021	0/0
1051	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006]UP JalNigam, UTTAR PRADESH	05/2017	767.59 -	09/2021 -	09/2021	0/0
1052	INTEGRATED PROJECT FOR DEVELOPMENT OF STPS IN ALLAHABAD ALONG WITH EXISTING ASSETS - [N30000007]UP JalNigam, UTTAR PRADESH	03/2018	904.00 -	09/2021 -	09/2021	0/0
1053	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010]UP JalNigam, UTTAR PRADESH	03/2018	967.23 -	09/2021 -	09/2021	0/0
1054	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022]UP JalNigam, UTTAR PRADESH	01/2019	206.05 -	10/2021 -	10/2021	0/0
1055	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]UP JalNigam, UTTAR PRADESH	01/2019	231.79 -	12/2021 -	12/2021	0/0
1056	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]UP JalNigam, UTTAR PRADESH	10/2017	213.62 261.12	03/2022 -	03/2022	0/0
1057	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]UP JalNigam, UTTAR PRADESH	02/2019	681.78 -	06/2022 -	06/2022	0/0
1058	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]UP JalNigam, UTTAR PRADESH	03/2019	298.12 213.91	07/2021 -	06/2022	0/0
1059	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR - [N30000009]UP JalNigam, UTTAR PRADESH	10/2016	370.40 430.49	08/2020 03/2021	-	0/0
	<u>Uttarakhand Pey Jal Nigam</u>					
1060	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI - [N30000003]UK JalNigam, UTTARAKHAND	03/2017	273.37 -	08/2019 -	-	0/0
1061	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH - [N30000004]UK JalNigam, UTTARAKHAND	03/2017	158.00 -	11/2019 03/2021	-	0/0
	<u>COMMERCE</u>					
	<u>National Building Construcion Corporation Ltd</u>					
1062	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI - [N40000003]NBCC, DELHI	06/2018	302.64 -	10/2020 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>HUMAN RESOURCE DEVELOPMENT</u>					
	<u>Central Public Works Department</u>					
1063	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH	11/2017	171.72 -	03/2020 -	06/2021	0/0
1064	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE,KANJIKODE WEST, DISTRICT PALAKKA - [N28000140]CPWD,KERALA	07/2019	753.63 -	03/2021 -	06/2022	0/0
1065	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR - [N42000008]CPWD,HIMACHAL PRADESH	09/2018	392.51 -	06/2022 -	06/2022	0/0
1066	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130]CPWD,JAMMU AND KASHMIR	03/2019	329.00 -	07/2022 -	07/2022	0/0
1067	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I. - [N28000141]CPWD,CHHATTISGARH	03/2020	808.62 -	07/2022 -	07/2022	0/0
1068	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A) - [N42000006]CPWD,KARNATAKA	07/2019	851.00 851.00	03/2022 -	09/2022	0/0
1069	PERMANENT CAMPUS FOR IIM BODH GAYA - [N42000009]CPWD,BIHAR	09/2018	375.00 -	09/2020 -	11/2022	0/0
1070	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRIC - [N42000007]CPWD,ANDHRA PRADESH	09/2019	588.72 -	09/2022 -	01/2023	0/0
1071	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]CPWD,JAMMU AND KASHMIR	01/2018	676.00 -	04/2023 -	04/2023	0/0
1072	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED - [N28000146]CPWD,WEST BENGAL	03/2020	193.83 -	06/2020 -	-	0/0
	<u>Edcil(India) Limited</u>					
1073	STUDY IN INDIA - [N42000003]EDCIL,MULTI STATE	03/2018	150.00 -	04/2018 -	-	0/0
	<u>Indian Institute Of Technology, Kharagpur</u>					
1074	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION - [N42000004]IITKGP,MULTI STATE	08/2018	418.00 -	03/2019 -	-	0/0
	<u>Rail India Technical And Economic Service</u>					
1075	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]RITES,MEGHALAYA	09/2013	484.32 -	09/2014 -	-	0/0
	<u>HOME AFFAIRS</u>					
	<u>Central Public Works Department</u>					
1076	CONSTRUCTION OF SEPARATE FAMILY ACCOMMODATION (440 NOS.) (PHASE-C/O 336 NOS. TYPE- II QTRS , 96 - [N45000001]CPWD,HARYANA	01/2020	166.98 -	05/2022 -	05/2022	0/0
1077	BUILDING OF THE FORCE HEADQUARTER INCLUDING SECTOR HQ RAF - [N45000002]CPWD,DELHI	06/2019	277.35 -	07/2022 -	07/2022	0/0
1078	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE- - [N28000147]CPWD,HARYANA	01/2020	166.98 167.00	10/2023 -	10/2023	0/0
	<u>DPIIT</u>					
	<u>Delhi Mumbai Industrial Corridor</u>					
1079	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]DMIC,MULTI STATE	09/2011	12,579.09 -	09/2019 01/2014	07/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2021)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>India International Convention And Expo Centre</u>					
1080	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]IICC,DELHI	11/2017	4,773.00 -	12/2019 -	12/2021	0/0
	Total		13,06,637.21 -			0/0
	Grand Total		13,06,637.21			0/0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above					(April 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>National Highways Authority Of India</u>							
1	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - PPP (ANNUITY) - [N24000176]	05/2010	374.00 -	166.90	05/2013 -	08/2021	-55.37	99
2	GWALIOR-JHANSI, NH-75 - PPP (ANNUITY) - [N24000089]	12/2003	604.00 -	364.59	12/2009 -	-	-39.64	0
3	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - PPP (BOT) - [N24000208]	07/2012	291.36 -	469.31	01/2014 -	12/2020	61.08	83
4	INDORE-DEWAS(NH-3) - PPP (BOT) - [N24000159]	11/2010	325.00 -	475.00	05/2013 -	-	46.15	0
5	DELHI/ HARYANA BORDER TO ROHTAK - PPP (BOT) - [N24000122]	04/2007	486.00 -	486.00	05/2010 -	-	.00	0
6	TRICHY - KARUR - PPP (BOT) - [N24000528]	03/2007	516.00 -	516.00	07/2008 -	-	.00	0
7	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - PPP (BOT) - [N24000426]	11/2012	530.07 -	530.07	08/2016 -	06/2020	.00	46
8	TIRUPATI - TIRUTHANI - CHENNAI - PPP (BOT) - [N24000178]	04/2011	571.00 -	571.00	10/2013 -	-	.00	0
9	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - PPP (BOT) - [N24000185]	09/2011	574.00 -	574.00	03/2014 -	-	.00	0
10	4-LANNING OF CHAPRA-HAJIPUR - PPP (ANNUITY) - [N24000187]	01/2011	575.00 -	575.00	07/2013 -	-	.00	0
11	2 LANNING OF MUZAFFARPUR - SONBARSA - PPP (ANNUITY) - [N24000188]	05/2011	511.54 -	591.00	11/2013 -	01/2021	15.53	86
12	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - PPP (BOT) - [N24000149]	02/2010	617.00 -	617.00	08/2012 -	-	.00	0
13	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - PPP (ANNUITY) - [N24000213]	04/2012	624.00 -	624.00	04/2014 -	01/2022	.00	93
14	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - PPP (BOT) - [N24000586]	06/2016	637.18 -	637.18	06/2019 -	09/2019	.00	3
15	PATNA-MUZZAFFARPUR - PPP (ANNUITY) - [N24000165]	08/2010	671.30 -	671.30	02/2013 -	-	.00	0
16	MUZZAFFARNAGAR-HARIDWAR - PPP (BOT) - [N24000201]	09/2011	754.00 -	754.00	03/2013 -	-	.00	0
17	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - PPP (BOT) - [N24000587]	06/2016	763.23 -	763.23	06/2019 -	-	.00	0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above (April 2021)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
18	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - PPP (BOT) - [N24000445]	08/2014	822.90	822.90	04/2018	-	.00	0
19	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - PPP (BOT) - [N24000454]	06/2014	923.04	923.04	11/2016	-	.00	0
20	KANDLA - MUNDRA PORT - PPP (BOT) - [N24000175]	01/2011	953.88	953.88	07/2013	-	.00	0
21	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - PPP (BOT) - [N24000453]	01/2015	972.50	972.50	07/2017	-	.00	0
22	4-LANING OF BRAHAMPUR-FARAKA - PPP (BOT) - [N24000203]	02/2011	998.79	998.79	08/2013	06/2022	.00	106
23	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - PPP (BOT) - [N24000205]	12/2011	1,047.00	1,047.00	06/2014	-	.00	81
24	4-LANING OF FARAKA-RAIGANJ - PPP (BOT) - [N24000202]	02/2011	1,078.84	1,078.84	08/2013	05/2021	.00	93
25	SRINAGAR TO BANIHAL - PPP (ANNUITY) - [N24000189]	06/2011	1,100.70	1,100.70	06/2014	10/2020	.00	76
26	GHAZIABAD-ALIGARH NH-91 - PPP (BOT) - [N24000170]	02/2011	1,141.00	1,141.00	08/2013	-	.00	0
27	INDORE-JHABUA-GUJRAT/MP - PPP (BOT) - [N24000136]	10/2010	1,175.00	1,175.00	04/2013	-	.00	0
28	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - PPP (BOT) - [N24001300]	11/2019	1,226.88	1,226.88	02/2021	-	.00	0
29	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - PPP (BOT) - [N24000172]	09/2011	1,250.00	1,250.00	12/2013	-	.00	0
30	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - PPP (BOT) - [N24000230]	05/2013	1,348.20	1,348.20	02/2014	-	.00	0
31	FOUR LANING OF HOSPET - CHITRADURGA - PPP (BOT) - [N24000490]	03/2015	1,388.00	1,388.00	08/2018	-	.00	0
32	6-LANING OF DHANKUNI-KHARAGPUR SECTION - PPP (BOT) - [N24000206]	04/2012	1,396.18	1,396.18	09/2014	-	.00	0
33	PANIKHOLI-RIMOLI - PPP (BOT) - [N24000197]	03/2012	1,410.00	1,410.00	09/2014	-	.00	0
34	RANCHI-RARGA-JAMSETHPUR - PPP (ANNUITY) - [N24000215]	12/2012	1,479.00	1,479.00	06/2015	-	.00	0
35	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - PPP (BOT) - [N24000125]	03/2010	1,509.10	1,509.10	09/2012	-	.00	0
36	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - PPP (BOT) - [N24000183]	11/2011	1,535.00	1,535.00	05/2014	-	.00	0
37	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - PPP (BOT) - [N24000233]	04/2014	1,266.60	1,544.00	09/2016	-	21.90	0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above (April 2021)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
38	ETAWAH CHAKERI - PPP (BOT) - [N24000219]	03/2013	1,573.00 -	1,573.00	09/2015 -	-	.00	0
39	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - PPP BOT (Hybrid Annuity) - [N24001301]	11/2019	1,601.10 -	1,601.10	02/2021 -	-	.00	0
40	FOUR LANING OF GWALIOR-SHIVPURI - PPP (BOT) - [N24000494]	05/2013	1,055.00 -	1,601.77	11/2015 -	-	51.83	0
41	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - PPP (BOT) - [N24000462]	05/2014	1,655.01 -	1,655.01	08/2016 -	12/2020	.00	52
42	6 LANING OF AGRA - ETAWAH BYPASS - PPP (BOT) - [N24000452]	07/2015	1,657.20 -	1,657.20	01/2019 -	-	.00	0
43	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - PPP (BOT) - [N24000477]	02/2008	1,673.70 -	1,673.70	10/2011 -	-	.00	0
44	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - PPP (BOT) - [N24000131]	02/2009	1,693.75 -	1,693.75	08/2011 -	-	.00	0
45	PUNE-SATARA(NH-4) - PPP (BOT) - [N24000156]	10/2010	1,724.55 -	1,724.55	03/2013 -	03/2021	.00	96
46	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - PPP (ANNUITY) - [N24000163]	07/2010	1,813.76 -	1,813.76	07/2013 -	-	.00	0
47	FOUR LANING OF AURANGABAD - YEDISHI - PPP (BOT) - [N24000508]	07/2015	1,871.34 -	1,871.34	01/2018 -	-	.00	0
48	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - PPP (BOT) - [N24000232]	11/2013	1,916.79 -	1,916.79	11/2016 -	-	.00	0
49	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - PPP (ANNUITY) - [N24000161]	07/2010	1,987.00 -	1,987.00	07/2015 -	09/2020	.00	62
50	AHMEDABAD TO VADODARA SECTION - PPP (BOT) - [N24000222]	01/2013	2,125.24 -	2,125.24	12/2015 -	-	.00	0
51	8 LANING OF MUKARBA CHOWK TO PANIPAT - PPP (BOT) - [N24000449]	07/2015	2,128.72 -	2,128.72	04/2019 -	09/2021	.00	29
52	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - PPP BOT (Hybrid Annuity) - [N24001185]	11/2017	2,159.00 -	2,159.00	01/2019 -	-	.00	0
53	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - PPP (BOT) - [N24000425]	07/2015	2,288.18 -	2,288.18	05/2019 -	-	.00	0
54	SIX-LANING OF BARWA ADDA-PANAGARH - PPP (BOT) - [N24000515]	04/2014	1,665.00 -	2,360.65	-	-	41.78	0
55	4 LANING OF NAGPUR-BETUL - PPP (ANNUITY) - [N24000155]	02/2011	2,498.76 -	2,498.76	08/2014 -	-	.00	0
56	NASHRI- CHANANI - PPP (ANNUITY) - [N24000162]	05/2011	2,159.00 -	2,519.00	06/2015 -	-	16.67	0
57	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - PPP (BOT) - [N24000133]	05/2009	1,108.00 -	2,967.50	11/2011 -	-	167.82	0
58	DELHI AGRA APPROVED LENGTH 180.0 KM - PPP (BOT) - [N24000224]	10/2012	1,928.22 -	3,182.34	04/2015 -	06/2021	65.04	74

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above (April 2021)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
59	VARANASI-AURANGABAD KM.786 TO KM.978.40 - PPP (BOT) - [N24000182]	09/2011	2,848.00 -	3,379.45	03/2014 -	12/2022	18.66	105
	Total		74,577.61 -	80,063.40				
	Grand Total		74,577.61	80,063.40				

Details of On Schedule Projects w.r.t. Original Schedule

Annexure - IV

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
1	CO CIVIL AVIATION RESEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD - [N04000086]	5/2020	353.61 -	353.61	61.13	05/2022 -	05/2022
2	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT - [N04000088]	1/2018	1,405.00 -	1,405.00	250.63	08/2022 -	08/2022
3	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	7/2018	346.27 -	480.33	51.11	09/2021 -	09/2021
4	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT - [N04000091]	4/2020	611.80 -	611.80	21.25	03/2023 -	03/2023
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICATION - [N04000079]	3/2017	475.39 -	475.39	88.11	04/2021 -	04/2021
	Total		3,192.07 -	3,326.13	472.23		
	<u>COAL</u>						
	<u>Central Coal Fields Limited</u>						
6	NORTH URIMARI EXPANSION OCP - [N06000182]	3/2019	1,553.06 -	1,553.06	277.47	03/2023 -	03/2023
7	TETARIAKHAR EXPANSION OCP - [N06000186]	11/2019	243.52 -	243.52	39.79	03/2023 -	03/2023
	<u>Eastern Coal Fields Limited</u>						
8	TILABONI UG MINE - [N06000172]	2/2019	916.62 -	916.62	0.61	03/2027 -	03/2027
9	NAKRAKONDA KUMARDIH B OCP - [N06000170]	8/2018	502.68 -	502.68	12.62	03/2029 -	03/2029
10	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT - [N06000191]	4/2020	483.65 -	483.65	1.82	03/2025 -	03/2025
11	SIDULI MINE (OC AND UG) - [N06000165]	5/2018	535.18 -	535.18	1.39	03/2026 -	03/2026
12	CHITRA EAST (RCE) OCP - [N06000169]	8/2018	513.98 -	513.98	121.23	03/2024 -	03/2024
13	PARASEA- BELBAID REORGANISATION UG MINE - [N06000185]	7/2019	826.42 -	826.42	0.03	03/2027 -	03/2027
14	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	247.51	03/2022 -	03/2022
	<u>Mahanadi Coal Fields Limited</u>						
15	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]	11/2018	2,838.87 -	2,838.87	1,236.90	03/2029 -	03/2029
16	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]	5/2018	2,434.75 -	2,434.75	181.04	03/2027 -	03/2027
17	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	1,986.09	03/2026 -	03/2026

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Northern Coal Fields Limited</u>						
18	SEMARIA OPENCAST PROJECT - [N06000176]	5/2019	396.58 -	396.58	-	03/2026 -	03/2026
19	BLOCK-B EXPANSION OPENCAST PROJECT - [N06000184]	7/2019	998.71 -	998.71	-	03/2023 -	03/2023
20	NIGAHI EXPANSION OCP (15 TO 25 MTPA) - [N06000196]	11/2020	1,729.68 -	1,729.68	-	03/2025 -	03/2025
21	BINA KAKRI AMALGAMATION OCP 14 MTPA - [N06000192]	8/2020	836.42 -	836.42	60.07	03/2024 -	03/2024
	<u>South-Eastern Coal Fields Limited</u>						
22	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	2,745.45	03/2023 -	03/2023
23	JHIRIA WEST OPENCAST PROJECT - [N06000166]	11/2018	389.97 -	389.97	-	03/2026 -	03/2026
24	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	1.62	03/2022 -	03/2022
25	DIPKA OC EXPANSION 40 MTY - [N06000200]	12/2020	5,241.40 -	5,241.40	1,931.58	03/2029 -	03/2029
26	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]	6/2010	11,816.40 -	11,816.40	4,487.05	03/2023 03/2016	03/2023
27	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	9.09	03/2023 -	03/2023
28	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	152.93	03/2022 -	03/2022
29	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
30	MAHAMAYA OPENCAST PROJECT - [N06000164]	5/2018	410.26 -	410.26	28.26	03/2026 -	03/2026
31	PORDA CHINTAPANI OCP (10 MTY) - [N06000199]	12/2020	2,310.12 -	2,310.12	-	03/2029 -	03/2029
32	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
33	BAROUD OC EXPANSION (3-10 MTY) - [N06000197]	8/2020	2,309.80 -	2,309.80	275.61	03/2029 -	03/2029
34	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	75.96	03/2026 -	03/2026
35	JAMPALI OCP RCE - [N06000198]	5/2020	278.64 -	278.64	183.02	03/2024 -	03/2024
	<u>Western Coal Fields Limited</u>						
36	VISHNUPURI UG TO OC MINE - [N06000178]	7/2018	195.57 -	195.57	2.94	03/2025 -	03/2025
37	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	745.03	365.38	03/2025 -	03/2025
38	BHANEAGAON OC - [N06000121]	2/2015	187.94 -	409.68	86.81	03/2023 -	03/2023
39	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	404.45	246.02	03/2022 -	03/2022
40	GANDHIGRAM UG MINE - [N06000183]	8/2019	414.16 -	414.16	0.87	03/2026 -	03/2026

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		56,940.81 -	57,264.99	14,759.16		
	<u>FINANCE</u>						
	<u>Central Public Works Department</u>						
41	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]	11/2017	348.77 -	348.77	123.99	11/2021 -	11/2021
	Total		348.77 -	348.77	123.99		
	<u>HEALTH AND FAMILY WELFARE</u>						
42	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR - [N21000029]	3/2019	1,404.00 -	1,404.00	200.58	09/2023 -	09/2023
43	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]	3/2019	1,577.00 -	1,828.00	-	09/2025 -	09/2025
	<u>National Building Construcion Corporation Ltd</u>						
44	AIIMS BILASPUR - [N21000028]	4/2018	1,351.00 -	1,471.00	712.04	09/2021 -	09/2021
	Total		4,332.00 -	4,703.00	912.62		
	<u>HOME AFFAIRS</u>						
	<u>Central Public Works Department</u>						
45	CONSTRUCTION OF SEPARATE FAMILY ACCOMMODATION (440 NOS.) (PHASE- C/O 336 NOS. TYPE- II QTRS , 96 - [N45000001]	1/2020	166.98 -	166.98	0.29	05/2022 -	05/2022
46	BUILDING OF THE FORCE HEADQUARTER INCLUDING SECTOR HQR RAF - [N45000002]	6/2019	277.35 -	277.35	10.60	07/2022 -	07/2022
47	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE- - [N28000147]	1/2020	166.98 167.00	166.98	-	10/2023 -	10/2023
	Total		611.31 -	611.31	10.89		
	<u>HUMAN RESOURCE DEVELOPMENT</u>						
48	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR - [N42000008]	9/2018	392.51 -	392.51	38.44	06/2022 -	06/2022
49	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I. - [N28000141]	3/2020	808.62 -	808.62	57.42	07/2022 -	07/2022
50	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]	1/2018	676.00 -	676.00	-	04/2023 -	04/2023
51	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130]	3/2019	329.00 -	329.00	-	07/2022 -	07/2022
	Total		2,206.13 -	2,206.13	95.86		
	<u>PETROLEUM</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Bharat Petroleum Corporation Limited</u>						
52	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]	11/2018	248.55 -	248.55	109.38	06/2022 -	06/2022
53	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]	9/2018	11,130.00 -	11,130.00	379.09	03/2023 -	03/2023
54	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL - [N16000365]	12/2017	1,524.06 -	1,524.06	785.64	12/2021 -	12/2021
55	2ND GENERATION LIGNOCELLULOSIC BIOMASS ETHANOL BIOFUEL REFINERY AT BARGARH (ODISHA) - [N16000374]	8/2019	1,607.00 -	1,607.00	255.22	08/2022 -	08/2022
56	KEROSENE HYDROTREATER (KHT) UNIT INTEGRATED WITH EXISTING DIESEL HYDROTREATER (DHT) UNIT AT MUMBAI R - [N16000410]	8/2020	697.00 -	697.00	155.18	03/2023 -	03/2023
57	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY - [N16000397]	7/2020	640.00 -	640.00	326.57	12/2021 -	12/2021
	<u>Gas Authority Of India Limited</u>						
58	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329]	10/2017	226.45 -	226.45	110.99	10/2022 -	10/2022
59	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]	7/2017	182.20 -	182.20	78.03	07/2022 -	07/2022
60	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]	7/2017	243.53 -	243.53	115.28	07/2022 -	07/2022
61	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	345.15	200.77	04/2022 -	04/2022
62	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT - [N16000398]	6/2020	7,844.25 -	7,844.25	1,079.10	05/2023 -	05/2023
63	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]	10/2017	359.25 -	359.25	143.73	10/2022 -	10/2022
64	SRIKAKULAM ANGUL PIPELINE PROJECT - [N16000388]	9/2019	2,658.34 -	2,658.34	245.50	07/2022 -	07/2022
65	CITY GAS DISTRIBUTION, JAMSHEDPUR - [N16000389]	10/2017	221.45 -	221.45	92.99	10/2022 -	10/2022
66	DHAMRA HALDIA PIPELINE PROJECT - [N16000391]	3/2020	1,030.65 -	1,030.65	53.10	11/2022 -	11/2022
67	BARAUNI-GUWAHATI PIPELINE - [N16000334]	6/2018	3,308.00 -	3,060.00	2,272.30	12/2021 -	12/2021
	<u>Hindustan Petroleum Corporation Limited</u>						
68	SETTING UP OF PHASE LL FACILITIES FOR HPCL GREEN R AND D CENTRE AT BENGALURU - [N16000380]	6/2018	380.00 -	380.00	222.20	11/2021 -	11/2021
69	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367]	6/2019	2,166.38 -	2,166.38	922.06	06/2022 -	06/2022
70	BARMER PALANPUR PIPELINE - [N16000384]	11/2019	776.00 -	776.00	215.96	11/2022 -	11/2022
71	SULPHUR FORMING UNIT IN SRU - [N16000408]	10/2020	210.94 -	210.94	117.03	08/2021 -	08/2021
72	RUF PITCH LOADING GANTRY - [N16000406]	10/2020	332.61 -	332.61	0.01	11/2022 -	11/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
73	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369]	12/2018	854.00 -	854.00	150.14	12/2022 -	12/2022
74	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB - [N16000402]	5/2020	1,421.46 -	1,244.50	76.19	02/2023 -	02/2023
	<u>Indian Oil Corporation Limited</u>						
75	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]	4/2018	5,654.00 -	5,654.00	2,826.29	10/2021 -	10/2021
76	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]	3/2018	676.00 -	676.00	433.41	08/2022 -	08/2022
77	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]	8/2019	1,255.00 -	1,255.00	185.11	10/2021 -	10/2021
78	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	1,536.61	02/2022 -	02/2022
79	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY - [N16000382]	11/2019	5,251.00 -	5,251.00	192.50	05/2023 -	05/2023
80	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI - [N16000403]	10/2020	921.00 -	921.00	19.14	09/2023 -	09/2023
81	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY - [N16000396]	7/2020	13,805.00 -	13,805.00	92.75	01/2024 -	01/2024
82	LAB REVAMP AT GUJARAT REFINERY - [N16000377]	10/2019	403.00 -	403.00	103.74	12/2021 -	12/2021
83	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY - [N16000409]	9/2020	18,936.00 -	18,936.00	715.09	09/2024 -	09/2024
84	AUGMENTATION OF CTMPL - [N16000286]	12/2016	228.00 -	228.00	140.61	11/2021 -	11/2021
85	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY - [N16000395]	1/2020	202.16 -	202.16	18.34	07/2022 -	07/2022
86	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY - [N16000393]	6/2020	1,019.00 -	1,019.00	58.94	01/2023 -	01/2023
87	AUGMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM - [N16000411]	10/2020	1,614.00 -	1,614.00	-	08/2023 -	08/2023
88	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400]	6/2020	1,378.00 -	1,378.00	24.39	12/2022 -	12/2022
89	LPG BP PROJECT CHITTOOR - [N16000381]	7/2019	167.00 -	167.00	8.89	07/2022 -	07/2022
90	MUZAFFARPUR-MOTIHARI LPG PIPELINE - [N16000399]	6/2020	403.00 -	403.00	1.77	08/2022 -	08/2022
91	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA - [N16000386]	1/2020	14,810.00 -	14,810.00	934.70	04/2023 -	04/2023
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
92	DEVANGONTHI MARKETING TERMINAL - [N16000401]	6/2020	200.00 -	200.00	2.26	06/2023 -	06/2023
	<u>Numaligarh Refinery Limited</u>						
93	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINERY - [N16000379]	1/2019	12,366.00 -	12,366.00	168.82	10/2024 -	10/2024

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
94	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES - [N16000394]	1/2019	10,228.00 -	10,228.00	117.34	10/2024 -	10/2024
	<u>Oil & Natural Gas Corporation Limited</u>						
95	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	970.30	832.63	03/2026 -	03/2026
96	HEERA REDEVELOPMENT - PHASE III - [N16000360]	6/2019	2,494.68 -	2,354.72	1,421.11	03/2022 -	03/2022
97	REDEVELOPMENT OF NANDASAN FIELD - [N16000404]	2/2020	444.87 -	444.87	87.40	08/2022 -	08/2022
98	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]	2/2017	4,006.83 -	3,596.00	3,514.02	05/2021 05/2021	05/2021
	Total		1,37,919.71 -	1,36,809.36	21,542.32		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
99	RAMAGUNDAM FLOATING SOLAR 100 MW - [N18000284]	6/2019	401.90 -	401.90	-	04/2021 -	04/2021
100	ETTAYAPURAM SOLAR 230MW - [N18000290]	3/2020	1,316.22 -	1,316.22	-	09/2021 -	09/2021
101	FATEHGARH SOLAR 296MW - [N18000289]	3/2020	1,749.31 -	1,749.31	-	09/2021 -	09/2021
102	KAWAS SOLAR 56 MW - [N18000283]	8/2020	261.80 -	261.80	-	10/2021 -	10/2021
	<u>Satluj Jal Vidyut Nigam Limited</u>						
103	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]	3/2019	10,439.09 -	10,439.09	2,035.50	01/2024 -	01/2024
104	LUHRI HYDROELECTRIC PROJECT (STAGE1) - [N18000279]	11/2020	1,810.56 -	1,810.56	422.46	01/2026 -	01/2026
105	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	947.89	577.17	12/2021 -	12/2021
	Total		16,627.21 -	16,926.77	3,035.13		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
106	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]	2/2016	2,750.00 -	3,438.51	-	03/2024 -	03/2024
107	WARDHA-NANDED MAHARASHTRA - [N22000231]	4/2008	3,168.29 -	3,168.29	1,352.27	03/2023 -	03/2023
108	PUNE-NASIK (265 KM) - [N22000354]	2/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024
109	DAUND - MANMAD (236 KM) - [N22000360]	2/2016	1,876.00 -	2,081.27	445.15	03/2023 -	03/2023
110	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]	2/2016	9,968.00 -	9,968.00	-	03/2024 -	03/2024
	<u>North Central Railway</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
111	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]	3/2018	4,329.53 -	4,329.53	33.37	03/2023 -	03/2023
	<u>North Eastern Railway</u>						
112	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	3/2007	243.78 -	895.00	111.89	12/2021 -	12/2021
113	HATHUA-BHATNI (N L) (NER) - [220100319]	4/2005	230.03 -	230.03	277.14	12/2022 -	12/2022
114	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,295.42 -	1,295.42	1,111.50	03/2022 -	03/2022
	<u>National High Speed Rail Corporation Limited</u>						
115	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]	12/2015	1,08,000.00 -	1,08,000.00	12,039.69	12/2023 -	12/2023
	<u>Rail Vikas Nigam Ltd.</u>						
116	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501]	6/2016	3,677.76 -	3,677.76	446.65	12/2023 -	12/2023
117	VIJAYAWADA-GUDUR - [N22000369]	4/2015	3,246.26 -	3,548.68	2,224.17	12/2023 -	12/2023
118	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	773.94 -	850.00	705.50	12/2024 -	12/2024
119	AHMEDABAD-BOTAD (GC) - [N22000140]	4/2012	975.62 -	1,500.00	1,497.74	12/2021 -	12/2021
	Total		1,42,959.63 -	1,48,324.17	20,245.07		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
120	BHOGAN KHURD TO KASHEDI - [N24001132]	9/2017	743.21 743.00	743.21	193.08	06/2021 -	06/2021
121	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307]	1/2017	197.67 -	197.67	5.75	12/2022 -	12/2022
122	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180]	3/2019	237.51 -	237.51	60.04	12/2022 -	12/2022
123	NAGPUR-BIKANER SECTION FROM KM 177.00 TO KM 267.325 ON NH-89 - [N24001240]	3/2020	370.36 -	370.36	90.45	08/2022 -	08/2022
124	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I - [N24001216]	12/2016	196.00 -	196.00	47.95	09/2021 -	09/2021
125	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197]	3/2018	351.00 -	351.00	128.70	06/2021 -	06/2021
126	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152]	9/2018	160.00 -	160.00	101.70	09/2021 -	09/2021
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
127	CONSTRUCTION, OPERATION AND MAINTENANCE OF Z-MORH TUNNEL INCLUDING APPROACHES ON NH-01 SRINAGAR-SONA - [N24001253]	12/2019	2,680.42 -	2,680.42	-	12/2023 -	12/2023
128	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG - [N24001257]	8/2020	159.85 -	159.85	-	10/2022 -	10/2022
129	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI - [N24001274]	8/2020	379.39 -	379.39	-	04/2022 -	04/2022
130	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL - [N24001264]	7/2020	228.39 -	228.39	-	04/2022 -	04/2022
131	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800 - [N24001248]	8/2020	208.84 -	208.84	-	04/2022 -	04/2022
132	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO - [N24001275]	8/2020	268.98 -	268.98	-	04/2022 -	04/2022
133	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68. - [N24001244]	8/2020	301.06 -	301.06	-	04/2022 -	04/2022
134	2-LANING FROM MANU-SIMLUNG (PKG I) - [N24001247]	3/2020	247.76 -	247.76	2.60	01/2022 -	01/2022
135	CONSTRUCTION & UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24001262]	7/2020	345.38 -	345.38	-	04/2023 -	04/2023
136	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) - [N24001272]	3/2020	167.95 -	167.95	1.12	06/2022 -	06/2022
137	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D - [N24001288]	8/2020	232.29 -	232.29	-	04/2022 -	04/2022
138	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54 - [N24001277]	9/2020	275.02 -	275.02	14.15	10/2022 -	10/2022
139	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K - [N24001266]	7/2020	210.79 -	210.79	-	04/2022 -	04/2022
140	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D - [N24001256]	8/2020	6,808.69 -	6,808.69	-	09/2026 -	09/2026
141	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) - [N24001273]	7/2020	177.76 -	177.76	0.64	08/2022 -	08/2022
142	2-LANING FROM MANU-SIMLUNG (PKG III) - [N24001249]	6/2020	347.36 -	347.36	-	01/2022 -	01/2022
143	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III) - [N24001284]	3/2020	361.53 -	361.53	13.17	06/2022 -	06/2022
144	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N - [N24001251]	3/2019	402.94 -	402.94	-	04/2022 -	04/2022
145	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 - [N24001252]	8/2020	295.97 -	295.97	-	04/2023 -	04/2023

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
146	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) - [N24001287	4/2020	330.80 -	330.80	11.57	12/2021 -	12/2021
147	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II) - [N24001279	3/2020	216.49 -	216.49	28.93	07/2022 -	07/2022
148	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) - [N24001269	3/2020	216.49 -	216.49	3.35	03/2022 -	03/2022
149	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV) - [N24001283	3/2020	281.78 -	281.78	38.40	07/2022 -	07/2022
150	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) - [N24001270	3/2020	292.24 -	292.24	1.74	06/2022 -	06/2022
151	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO - [N24001245	9/2020	353.90 -	353.90	4.21	05/2022 -	05/2022
152	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) - [N24001271	6/2020	365.53 -	365.53	3.35	08/2022 -	08/2022
153	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) - [N24001278	3/2020	206.88 -	206.88	9.33	07/2022 -	07/2022
154	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID - [N24001267	3/2020	178.43 -	178.43	-	07/2022 -	07/2022
155	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM - [N24001259	9/2020	315.63 -	315.63	-	04/2022 -	04/2022
156	CONSTRUCTION & UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24001261	8/2020	311.00 -	311.00	-	04/2023 -	04/2023
157	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T - [N24001260	9/2020	257.15 -	257.15	17.77	04/2022 -	04/2022
158	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 - [N24001254	3/2020	242.97 -	242.97	-	06/2022 -	06/2022
159	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAPOKPI TO SEKMAI SECTI - [N24001276	8/2020	228.97 -	228.97	-	04/2022 -	04/2022
160	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137 - [N24001268	3/2019	471.00 -	471.00	-	07/2022 -	07/2022
161	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D - [N24001255	9/2020	277.44 -	277.44	-	10/2022 -	10/2022
162	4-LANING OF HAPACHARA - TULUNGIA SECTION - [N24001246	3/2020	220.20 -	220.20	-	12/2022 -	12/2022
163	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I) - [N24001280	3/2020	320.97 -	320.97	18.73	06/2022 -	06/2022
164	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) - [N24001286	3/2020	278.95 -	278.95	56.76	06/2022 -	06/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
165	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV) - [N24001285	3/2020	330.78 -	330.78	23.74	12/2021 -	12/2021
166	REHABILITATION & UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE SE - [N24001265	3/2020	154.51 -	154.51	-	07/2022 -	07/2022
167	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) - [N24001282	3/2020	355.79 -	355.79	31.76	06/2022 -	06/2022
168	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES - [N24001258	8/2020	202.36 -	202.36	-	04/2022 -	04/2022
169	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) - [N24001281	3/2020	292.24 -	292.24	29.00	07/2022 -	07/2022
170	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923 - [N24001250	8/2020	278.46 -	278.46	12.06	03/2022 -	03/2022
171	REHABILITATION & UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION - [N24001263	6/2020	277.50 -	277.50	-	01/2022 -	01/2022
	<u>National Highways Authority Of India</u>						
172	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA - [N24001302	7/2020	3,426.00 -	3,426.00	-	12/2021 -	12/2021
173	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN - [N24001306	10/2020	724.60 -	724.60	-	03/2023 -	03/2023
	Total		27,765.18 -	27,765.18	950.05		
	<u>RURAL DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
174	CONSTRUCTION OF GRAMEEN VIKAS BHAWAN (2BASEMENTS+ GROUND+9 FLOORS) FOR MINISTRY OF RURAL DEVELOPMENT - [N28000132	11/2018	361.60 -	361.60	12.44	07/2021 -	07/2021
	Total		361.60 -	361.60	12.44		
	<u>SHIPPING AND PORTS</u>						
	<u>Inland Waterways Authority Of India</u>						
175	JAL MARG VIKAS PROJECT - [N25000072	1/2018	5,369.18 -	4,633.81	1,871.35	03/2023 -	03/2023
	Total		5,369.18 -	4,633.81	1,871.35		
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
176	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 - [N12000124	11/2015	2,907.00 -	2,907.00	256.24	06/2023 -	06/2023
	<u>Steel Authority Of India Limited (Sail)</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
177	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP - [N12000123]	11/2020	542.24 -	542.24	31.68	12/2023 -	12/2023
178	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY - [N12000122]	11/2020	377.18 -	377.18	32.76	05/2023 -	05/2023
	Total		3,826.42 -	3,826.42	320.68		
	<u>URBAN DEVELOPMENT</u>						
	<u>Ahmedabad Metro Rail</u>						
179	SURAT METRO RAIL PROJECT - [N28000138]	3/2019	12,020.32 -	12,020.32	20.65	03/2024 -	03/2024
180	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137]	3/2019	5,384.17 -	5,384.17	63.77	03/2024 -	03/2024
	<u>Central Public Works Department</u>						
181	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]	10/2016	1,128.00 -	1,128.00	22.00	03/2022 -	03/2022
	<u>Delhi Metro Rail Corporation</u>						
182	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS - [N28000135]	7/2019	24,948.65 -	24,948.65	1,763.02	03/2025 -	03/2025
	<u>Lucknow Metro Rail Corporation Limited</u>						
183	KANPUR METRO RAIL PROJECT - [N28000144]	5/2019	11,076.48 -	11,076.48	-	03/2024 -	03/2024
184	AGRA METRO RAIL PROJECT - [N28000145]	5/2019	8,379.62 -	8,379.62	-	03/2024 -	03/2024
	<u>Maharashtra Metro Rail Corporation Ltd.</u>						
185	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]	12/2016	11,420.00 -	11,420.00	6,214.58	11/2021 -	11/2021
	<u>Madhya Pradesh Metro Rail Co Limited</u>						
186	BHOPAL METRO RAIL - [N28000124]	11/2018	6,941.40 -	6,941.40	174.53	02/2023 -	02/2023
187	INDORE METRO RAIL - [N28000125]	11/2018	7,500.80 -	7,500.80	130.21	02/2023 -	02/2023
	<u>National Capital Region Transport Corp</u>						
188	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134]	3/2019	30,274.00 -	30,274.00	3,416.31	06/2025 -	06/2025
	<u>Patna Metro Rail Corporation</u>						
189	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]	2/2019	13,365.77 -	13,365.77	231.97	06/2024 -	06/2024
	Total		1,32,439.21 -	1,32,439.21	12,037.04		
	<u>WATER RESOURCES</u>						
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>						
190	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA - [N30000051]	8/2017	824.00 -	824.00	40.09	06/2022 -	06/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
191	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]	5/2017	356.37 -	356.37	93.34	04/2021 -	04/2021
192	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]	3/2017	277.42 -	277.42	146.23	05/2021 -	05/2021
193	SEWER NETWORKS, SPS AND STP, MUNGER - [N30000036]	3/2018	294.02 -	294.02	-	10/2021 -	10/2021
194	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]	8/2017	578.89 -	578.89	40.09	06/2022 -	06/2022
195	SEWERAGE SCHEME AT PAHARI ZONE IVA S PATNA - [N30000041]	5/2017	184.86 -	184.86	152.78	05/2021 -	05/2021
196	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026]	3/2018	230.06 -	230.06	73.63	07/2021 -	07/2021
	<u>Delhi Jal Board</u>						
197	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014]	3/2017	665.78 -	665.78	194.55	12/2022 -	12/2022
	<u>Kolkata Metropolitan Development Authority</u>						
198	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]	8/2017	185.22 -	185.22	-	12/2021 -	12/2021
199	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]	1/2019	384.96 -	384.96	-	04/2022 -	04/2022
200	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPUR - [N30000030]	3/2019	287.53 -	287.53	-	04/2022 -	04/2022
201	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033]	3/2018	165.16 -	165.16	-	06/2022 -	06/2022
202	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA - [N30000034]	8/2017	307.12 -	307.12	-	09/2022 -	09/2022
203	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]	10/2017	164.93 -	164.93	-	12/2021 -	12/2021
204	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048]	1/2018	172.10 -	172.10	-	12/2021 -	12/2021
205	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]	12/2018	234.31 -	234.31	-	04/2022 -	04/2022
	<u>Uttar Pradesh Jal Nigam</u>						
206	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH - [N30000013]	3/2019	271.39 -	271.39	-	08/2021 -	08/2021
207	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]	10/2017	213.62 -	261.12	-	03/2022 -	03/2022
208	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]	1/2019	231.79 -	234.03	-	12/2021 -	12/2021
209	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]	2/2019	681.78 -	690.71	-	06/2022 -	06/2022
210	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022]	1/2019	206.05 -	206.05	29.26	10/2021 -	10/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
211	INTEGRATED PROJECT FOR DEVELOPMENT OF STPS IN ALLAHABAD ALONG WITH EXISTING ASSETS - [N30000007	3/2018	904.00 -	904.00	136.55	09/2021 -	09/2021
212	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010	3/2018	967.23 -	967.23	40.59	09/2021 -	09/2021
213	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006	5/2017	767.59 -	767.59	76.71	09/2021 -	09/2021
	Total		9,556.18 -	9,614.85	1,023.82		
	Grand Total		5,44,455.41	5,49,161.70	77,412.65		

List of Projects in which Expenditure is More than Approved Cost

Annexure - II

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	9/2003	3,492.00 -	6,840.00	5,935.96	09/2010 09/2016	10/2022
	<u>Nuclear Power Corporation Of India Limited</u>						
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	16,488.00	12/2015 -	02/2022
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]	10/2009	12,320.00 -	17,079.00	13,206.00	12/2016 -	03/2023
	Total		27,271.00 -	40,499.00	35,629.96		
	<u>COAL</u>						
	<u>Singareni Colliers Company Limited</u>						
4	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	7/2011	162.76 -	349.28	251.14	03/2015 -	03/2022
	<u>Western Coal Fields Limited</u>						
5	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]	2/2016	198.68 -	325.18	253.17	03/2019 -	03/2022
	Total		361.44 -	674.46	504.31		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation Ltd</u>						
6	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	2/2013	414.11 -	499.23	494.72	11/2013 -	05/2021
7	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]	7/2016	152.95 -	177.92	164.17	02/2018 -	03/2021
8	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	8/2017	272.19 -	272.54	272.54	03/2019 -	03/2021
9	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	9/2014	505.58 -	585.00	586.96	03/2018 -	09/2019
10	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]	12/2014	168.90 -	191.20	169.51	05/2017 -	07/2019
11	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 -	250.00	240.24	05/2017 -	03/2021
12	AIIMS - OPD(NEW) - [N21000009]	8/2014	293.65 -	325.00	299.76	05/2017 -	01/2020
	Total		2,011.82 -	2,300.89	2,227.90		
	<u>PETROLEUM</u>						
	<u>Oil India Limited</u>						

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
13	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	7/2011	352.56 -	490.24	455.00	03/2017 -	03/2021
	Total		352.56 -	490.24	455.00		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
14	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	15,105.22	13,657.43	01/2018 -	02/2021
15	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	11,148.86	10,019.31	01/2020 -	-
16	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	13,766.78	10/2017 -	-
17	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]	4/2012	9,750.89 -	12,176.28	11,130.00	02/2017 -	01/2021
	<u>North East Electric Power Corporation</u>						
18	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	7,927.34	8,225.88	12/2009 02/2021	-
	<u>Power Grid Corporation Of India Limited</u>						
19	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	590.30	06/2014 -	-
	Total		46,090.34 -	59,736.98	57,389.70		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
20	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	4/2011	184.06 -	315.00	312.62	03/2019 -	-
21	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	2/1997	2,271.50 -	4,517.49	2,648.51	03/2021 -	03/2023
	<u>Container Corporation Of India</u>						
22	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]	1/2013	387.70 -	487.13	434.63	03/2018 -	03/2021
	<u>East Central Railways</u>						
23	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	3/1999	1,033.07 -	3,550.00	3,567.20	- -	03/2022
24	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	4/2003	528.65 -	2,066.78	1,560.44	- -	03/2023
25	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]	4/1991	329.39 -	1,483.14	1,207.52	- -	03/2022
26	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]	4/1998	180.82 -	726.31	546.29	- -	-
27	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	1/1991	332.15 -	546.71	541.43	07/2014 -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
28	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	4/2013	213.01 -	480.00	486.66	- -	-
29	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]	4/2004	372.14 -	1,470.50	1,288.24	- -	03/2023
30	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	4/2006	378.56 -	1,858.75	386.35	- -	03/2023
31	SAKRI-HASANPUR ROAD (NL) - [N22000171]	4/1999	325.00 -	735.20	384.25	- -	03/2021
32	KODERMA-TILAIYA (NL), ECR - [220100305]	4/2002	459.91 -	1,625.87	758.44	- -	03/2023
33	HAJIPUR - BACHAWARA - [N22000334]	5/2015	678.54 -	929.86	848.39	03/2019 -	05/2021
34	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	4/1997	162.87 -	614.45	348.95	- -	12/2023
35	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	4/1997	324.73 -	1,070.00	1,069.58	03/2012 -	11/2022
36	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	4/1996	477.88 283.95	751.55	694.88	03/2012 -	07/2021
	<u>Eastern Railways</u>						
37	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	4/2000	607.09 -	1,425.44	638.05	02/2013 -	03/2024
38	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI- SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]	4/2010	365.17 -	439.30	411.65	03/2017 -	03/2025
39	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]	4/2011	175.80 -	495.10	288.51	- -	03/2022
40	MONIGRAM- NIMTITA - [N22000301]	4/2012	250.93 -	310.70	293.10	- -	03/2024
41	PIRPAINTI-BHAGALPUR - [N22000222]	4/2011	261.38 -	565.00	547.01	- -	05/2019
42	BANDEL-BOINCHI 3RD LINE - [N22000221]	4/2011	288.35 -	502.48	432.62	- -	03/2021
43	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	4/2012	255.64 -	272.20	261.26	- -	03/2022
	<u>Metropolitan Rapid Transport Projects</u>						
44	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	3/2000	1,049.69 -	3,404.92	3,837.57	12/2006 -	-
45	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	3/1996	495.44 -	2,980.41	1,768.25	03/2004 -	03/2022
46	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	4/2006	495.74 -	734.01	510.69	06/2013 06/2022	12/2021
47	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	3/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021
	<u>North Central Railway</u>						
48	ETAWAH-MAINPURI (NL),NCR - [220100318]	4/1997	120.00 -	346.00	345.51	12/2008 -	-
	<u>North East Frontier Railway</u>						

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
49	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	4/2000	1,180.19 -	4,541.38	3,804.55	12/2008 -	05/2021
50	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	9/2006	385.20 -	1,043.00	837.67	03/2019 -	03/2023
51	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	4/2003	4,454.17 -	12,264.15	10,994.55	03/2011 -	12/2023
52	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]	2/1999	380.60 -	1,090.60	1,089.12	04/2010 -	-
53	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	4/2016	602.27 -	2,144.78	921.83	12/2021 -	04/2021
54	DIGARU-HOJAI (102 KM) - [N22000389]	4/2015	870.96 -	1,873.21	1,309.41	03/2021 -	05/2021
55	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	4/2011	314.00 -	800.00	823.02	03/2019 -	03/2021
56	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	4/1999	819.23 -	1,871.00	1,082.01	- -	-
57	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	4/2010	241.52 -	373.87	287.09	- -	12/2021
<u>North Eastern Railway</u>							
58	HATHUA-BHATNI (N L) (NER) - [220100319]	4/2005	230.03 -	230.03	277.14	12/2022 -	12/2022
59	CHHAPRA-BALLIA UP - [N22000134]	3/2013	295.00 -	477.31	378.98	01/2019 -	02/2022
<u>North Western Railway</u>							
60	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	2/1997	410.08 -	860.41	709.62	02/2019 -	06/2022
61	AJMER-BANGURGRAM - [N22000155]	4/2011	213.39 -	375.00	348.55	11/2019 -	03/2021
62	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	4/2012	246.08 -	395.00	348.47	12/2019 -	02/2021
63	THIYAT HAMIRA-SANU - [N22000149]	4/2013	236.93 -	350.45	273.79	10/2018 -	01/2020
64	ALWAR-BANDIKUI DOUBLING - [N22000157]	4/2013	242.09 -	525.00	460.83	02/2019 -	02/2020
<u>Northern Railway</u>							
65	ROHTAK-MEHAM HANSI - [N22000272]	4/2012	287.00 -	893.45	705.53	12/2011 -	06/2021
66	NANGALDAM-TALWARA(NL),NR - [220100188]	3/1981	450.00 -	2,200.00	714.78	07/2012 -	03/2024
67	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	3/1995	2,500.00 -	27,949.00	24,040.61	11/2002 -	12/2022
68	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	3/2002	625.00 -	859.00	852.73	03/2016 -	06/2021
69	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]	4/2007	336.91 -	791.39	572.99	- -	03/2023
<u>Rail Vikas Nigam Ltd.</u>							

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
70	HARIDASPUR-PARADEEP(NL) - [220100285	4/1996	1,185.64 -	1,844.47	1,883.44	12/2017 -	-
71	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	4/1998	1,202.70 -	2,440.53	1,337.54	02/2015 -	06/2022
72	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	4/2000	133.41 207.00	396.00	388.21	03/2009 03/2009	-
73	BINA - KOTA DOUBLING WITH RE - [N22000414	4/2011	1,485.85 -	1,835.83	1,571.35	12/2020 -	12/2021
74	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413	3/2012	1,183.25 -	1,825.00	1,411.49	12/2020 -	12/2022
75	BANASPANI- JAKHPURA - DOUBLING - [N22000412	3/2009	942.95 -	1,536.00	1,089.84	03/2019 -	06/2022
76	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410	3/2006	948.04 -	2,009.00	1,875.48	03/2020 -	12/2021
77	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE- GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407	3/2009	713.48 -	2,725.00	2,554.71	03/2020 -	12/2021
78	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404	4/2011	927.01 -	1,400.00	1,331.76	03/2019 -	06/2022
79	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213	4/2012	632.68 -	950.00	810.96	03/2016 -	12/2021
80	PALANPUR-SAMAKHAYALI (DL) - [N22000144	4/2013	1,548.66 -	1,868.89	1,831.45	12/2021 -	03/2022
81	DHASA-JETALSAR (GC) - [N22000141	4/2012	644.38 -	872.65	800.30	03/2021 -	03/2021
82	AHMEDABAD-BOTAD (GC) - [N22000140	4/2012	975.62 -	1,500.00	1,497.74	12/2021 -	12/2021
83	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313	3/2012	1,503.71 -	3,377.00	2,683.67	03/2020 -	03/2022
84	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297	4/2010	2,127.00 -	3,000.00	2,208.46	03/2023 -	12/2022
	<u>South Central Railway</u>						
85	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192	3/1996	164.36 -	1,050.00	999.64	02/2009 -	-
86	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205	4/1997	1,723.00 1.00	3,421.35	1,895.77	03/2000 -	03/2023
	<u>South East Central Railway</u>						
87	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	4/2005	383.79 -	1,413.76	1,416.77	- -	-
88	GONDIA-JABALPUR(GC),(SECR) - [220100186	2/1997	511.86 -	2,005.25	1,777.22	04/2020 -	04/2021
89	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483	4/2008	872.00 -	1,226.51	1,131.91	12/2019 -	-
90	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438	4/2010	585.93 -	1,268.32	941.56	02/2019 -	12/2021
	<u>South Eastern Railway</u>						
91	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	4/2012	148.77 -	377.00	201.09	12/2016 -	08/2020

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>South Western Railway</u>						
92	HUBLI- CHIKJAJUR - [N22000325]	3/2015	1,156.94 -	1,656.00	1,160.49	03/2020 03/2023	03/2023
93	ARSIKERE-TUMKUR - [N22000332]	3/2015	578.00 -	783.00	620.29	03/2020 06/2021	06/2021
94	YELAHANKA-PENUKONDA - [N22000328]	5/2015	860.43 -	1,147.00	911.86	03/2020 -	06/2021
	<u>Southern Railway</u>						
95	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'- AGASTIYAMPALLI - [N22000079]	9/2007	724.69 -	2,910.84	1,621.40	02/2019 -	03/2025
96	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	9/1995	303.98 -	1,720.00	701.37	03/2020 -	03/2025
97	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	2/2015	760.00 -	1,536.00	1,233.08	03/2020 -	06/2022
98	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	2/1996	268.87 -	950.00	928.36	03/2005 -	09/2021
99	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]	10/2013	187.26 -	327.00	268.75	04/2014 -	12/2020
100	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	4/2011	120.70 -	2,172.16	262.36	03/2019 -	12/2027
101	MADURAI-BODINAYAKKANUR - [N22000201]	4/2008	164.41 -	608.13	375.67	- 10/2021	09/2021
102	KURUPPANTHARA-CHINGAVANAM - [N22000190]	4/2007	270.14 -	457.08	439.49	- -	12/2021
	<u>West Central Railway</u>						
103	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314]	4/2001	424.60 -	2,909.99	1,229.79	03/2021 03/2029	03/2023
104	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	9/1998	247.66 -	8,248.50	2,131.17	05/2008 -	03/2025
	<u>Western Railway</u>						
105	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]	4/2006	117.36 196.95	202.35	809.40	03/2011 -	-
	Total		59,929.57 -	1,69,157.91	1,27,478.43		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
106	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]	11/2010	624.41 -	992.67	890.74	03/2011 -	12/2020
107	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]	1/1991	282.41 -	322.01	327.21	08/2016 -	-
108	CONSTRUCTION OF FLYOVER FROM KM 604/252 TO 607/060 (MARTHANDAM JUNCTION) AND FROM KM 630/116 TO 631/ - [N24001238]	5/2016	307.70 -	307.70	312.82	01/2017 -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
109	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]	8/2010	186.96 -	322.24	298.52	09/2014 -	06/2021
110	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]	3/2018	325.86 -	325.86	326.88	10/2018 -	-
111	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]	10/2013	445.89 653.00	653.29	754.40	03/2017 -	04/2021
112	KALMATH TO ZARAP - [N24001137]	9/2016	1,338.13 1,338.00	1,338.13	1,346.39	03/2020 -	-
113	TALGAON TO KALMATH - [N24001136]	10/2016	904.70 905.00	904.70	969.90	03/2020 -	-
114	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]	3/2016	536.65 356.00	536.65	539.35	12/2019 06/2021	06/2021
115	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]	3/2018	256.15 -	256.15	262.63	12/2019 -	-
116	LATUR TO PANGAON - [N24001066]	3/2018	336.47 336.00	336.47	394.00	12/2019 -	-
117	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938]	3/2018	297.12 294.00	294.12	373.98	07/2018 -	-
118	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]	8/2015	288.24 -	288.24	303.16	11/2015 -	-
119	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]	12/2011	159.39 -	159.39	210.29	11/2017 -	-
120	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221.400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]	9/2012	511.00 -	511.00	2,323.04	10/2013 -	-
121	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]	8/2010	195.04 -	377.99	331.49	10/2010 -	06/2021
122	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]	11/2010	268.08 -	390.73	283.52	05/2017 -	-
123	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]	3/2015	298.33 -	298.33	310.72	- -	-
124	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]	8/2010	193.69 -	327.92	301.46	10/2010 -	06/2021
125	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]	10/2013	445.89 -	653.29	464.05	03/2017 -	-
126	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]	11/2013	497.05 -	881.05	754.27	05/2017 -	04/2021
127	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]	3/2012	207.03 -	389.45	308.09	05/2012 06/2018	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
128	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]	3/2015	394.00 -	394.00	400.56	06/2018 -	-
	<u>National Highways Authority Of India</u>						
129	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	520.00	612.58	02/2009 -	-
130	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]	4/2011	571.00 -	571.00	582.53	10/2013 -	-
131	KANDLA - MUNDRA PORT - [N24000175]	1/2011	953.88 -	953.88	976.79	07/2013 -	-
132	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]	9/2011	1,250.00 -	1,250.00	1,337.11	12/2013 -	-
133	GHAZIABAD-ALIGARH NH-91 - [N24000170]	2/2011	1,141.00 -	1,141.00	1,715.42	08/2013 -	-
134	PATNA-MUZZAFFARPUR - [N24000165]	8/2010	671.30 -	671.30	1,360.63	02/2013 -	-
135	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]	7/2010	1,813.76 -	1,813.76	2,652.11	07/2013 -	-
136	NASHRI- CHANANI - [N24000162]	5/2011	2,159.00 -	2,519.00	4,709.65	06/2015 -	-
137	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]	7/2010	1,987.00 -	1,987.00	3,108.90	07/2015 -	09/2020
138	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	4/2014	1,266.60 -	1,544.00	1,446.45	09/2016 -	-
139	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]	12/2015	611.65 -	611.65	728.24	06/2016 -	-
140	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]	6/2015	845.24 -	941.00	889.83	-	01/2020
141	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]	1/2015	972.50 -	972.50	1,492.00	07/2017 -	-
142	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]	7/2015	1,657.20 -	1,657.20	2,345.00	01/2019 -	-
143	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]	8/2014	822.90 -	822.90	1,688.16	04/2018 -	-
144	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]	10/2015	593.26 -	690.17	595.33	05/2018 06/2021	06/2021
145	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]	10/2015	531.13 -	730.97	653.06	05/2018 06/2021	06/2021
146	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]	11/2012	530.07 -	530.07	556.02	08/2016 -	06/2020
147	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]	2/2011	998.79 -	998.79	1,878.70	08/2013 -	06/2022

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
148	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517	12/2015	479.20 -	479.20	712.89	05/2018 -	-
149	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515	4/2014	1,665.00 -	2,360.65	4,472.01	- -	-
150	FOUR LANING FROM MPMHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509	4/2010	1,170.52 -	1,170.52	2,051.36	06/2012 -	-
151	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508	7/2015	1,871.34 -	1,871.34	3,443.43	01/2018 -	-
152	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503	10/2015	447.29 -	746.43	676.33	12/2017 -	-
153	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494	5/2013	1,055.00 -	1,601.77	1,393.40	11/2015 -	-
154	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477	2/2008	1,673.70 -	1,673.70	3,326.93	10/2011 -	-
155	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463	12/2015	1,083.00 -	1,827.15	2,082.19	06/2018 -	-
156	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462	5/2014	1,655.01 -	1,655.01	1,867.51	08/2016 -	12/2020
157	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624	9/2016	1,244.10 -	1,244.10	1,590.00	- -	05/2021
158	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623	9/2016	1,100.19 -	1,145.31	1,327.00	- -	03/2021
159	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622	9/2016	950.69 -	1,108.00	1,429.25	08/2019 -	-
160	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621	9/2016	1,239.82 -	1,727.66	1,674.80	- -	01/2021
161	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608	8/2016	248.97 -	248.97	270.65	05/2019 -	-
162	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601	8/2016	1,169.61 -	2,280.00	1,282.04	- -	-
163	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600	8/2016	1,388.34 -	2,587.50	1,569.38	09/2019 -	-
164	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591	7/2016	688.70 -	688.70	870.48	- -	-
165	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKPUR) - [N24000547	3/2016	1,404.50 -	1,404.50	2,977.58	- -	-
166	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214	12/2017	217.96 -	884.00	257.13	- -	-
167	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853	3/2018	642.13 -	807.00	666.56	- -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
168	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838	3/2018	874.25 -	874.25	886.59	- -	-
169	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810	3/2018	565.09 -	565.09	601.35	- -	02/2021
170	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793	3/2018	925.40 -	1,197.00	1,011.70	- -	-
171	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789	2/2018	2,177.80 -	2,450.00	2,244.98	- -	-
172	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787	2/2018	1,995.34 -	2,400.00	3,088.59	- -	11/2021
173	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713	12/2017	404.94 -	448.18	427.22	- -	10/2020
174	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	3/2017	993.16 -	1,434.00	1,201.43	03/2020 -	-
175	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	3/2017	831.58 -	1,177.00	912.40	03/2020 -	-
176	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	3/2017	2,064.99 -	2,447.00	2,357.84	03/2020 -	-
177	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	3/2017	988.34 -	1,043.28	1,035.00	03/2020 -	-
178	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650	1/2017	244.90 -	244.90	251.87	05/2019 -	-
179	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638	11/2012	605.84 -	722.46	722.46	07/2018 -	-
180	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634	10/2016	447.75 -	447.75	1,160.74	- -	08/2020
181	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546	2/2016	273.20 -	273.20	667.10	02/2019 -	-
182	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545	1/2016	1,134.97 -	1,134.97	1,634.05	11/2018 -	-
183	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544	3/2016	676.73 -	676.73	977.26	04/2019 -	-
184	MEERUT-BULANDSHAHR - [N24000539	1/2016	683.24 -	987.94	867.27	- -	-
185	TRICHY - KARUR - [N24000528	3/2007	516.00 -	516.00	886.96	07/2008 -	-
186	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522	8/2015	516.13 -	649.27	712.15	04/2018 -	-
187	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521	8/2015	854.80 -	1,038.56	1,160.00	- -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
188	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]	8/2015	275.90 -	275.90	289.13	- -	-
189	4-LANING OF FARAKA-RAIGANJ - [N24000202]	2/2011	1,078.84 -	1,078.84	2,295.18	08/2013 -	05/2021
190	MUZAFFARNAGAR-HARIDWAR - [N24000201]	9/2011	754.00 -	754.00	1,364.18	03/2013 -	-
191	PANIKHOLI-RIMOLI - [N24000197]	3/2012	1,410.00 -	1,410.00	1,935.14	09/2014 -	-
192	SRINAGAR TO BANIHAL - [N24000189]	6/2011	1,100.70 -	1,100.70	2,924.02	06/2014 -	10/2020
193	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]	10/2011	375.09 -	375.09	494.33	04/2014 -	-
194	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]	9/2011	574.00 -	574.00	768.73	03/2014 -	-
195	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]	11/2011	1,535.00 -	1,535.00	3,278.00	05/2014 -	-
196	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]	9/2011	2,848.00 -	3,379.45	2,901.20	03/2014 -	12/2022
197	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]	4/2014	495.78 -	627.93	633.24	01/2016 01/2020	01/2020
198	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]	4/2014	351.34 -	417.68	433.68	01/2016 12/2020	12/2020
199	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	3,182.34	3,087.00	04/2015 01/2021	06/2021
200	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	4,669.71	12/2015 -	-
201	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	2,093.25	09/2015 -	-
202	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]	4/2012	1,396.18 -	1,396.18	2,894.94	09/2014 -	-
203	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]	12/2011	1,047.00 -	1,047.00	1,874.43	06/2014 -	03/2021
204	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]	11/2013	1,916.79 -	1,916.79	1,960.92	11/2016 -	-
205	NALBARI TO BIJNI (AS-6) - [N24000047]	12/2003	225.00 -	225.00	390.72	06/2008 -	09/2019
206	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 -	230.00	370.56	04/2008 -	02/2021
207	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61 -	360.84	489.84	04/2010 -	07/2019
208	INDORE-DEWAS(NH-3) - [N24000159]	11/2010	325.00 -	475.00	469.54	05/2013 -	-
209	PUNE-SATARA(NH-4) - [N24000156]	10/2010	1,724.55 -	1,724.55	2,559.00	03/2013 -	03/2021
210	4 LANING OF NAGPUR-BETUL - [N24000155]	2/2011	2,498.76 -	2,498.76	2,531.46	08/2014 -	-
211	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]	2/2010	617.00 -	617.00	943.17	08/2012 -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
212	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131	2/2009	1,693.75 -	1,693.75	2,848.49	08/2011 -	-
213	INDORE-JHABUA-GUJRAT/MP - [N24000136	10/2010	1,175.00 -	1,175.00	1,509.96	04/2013 -	-
214	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125	3/2010	1,509.10 -	1,509.10	3,684.44	09/2012 -	-
215	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230	5/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	-
216	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	655.17	655.17	07/2009 -	-
217	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	5/2009	1,108.00 -	2,967.50	3,996.01	11/2011 -	-
218	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049	12/2003	160.00 -	167.98	233.27	05/2008 -	06/2019
219	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	340.14	325.28	04/2009 -	-
220	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279	12/2003	167.64 -	435.78	427.96	11/2008 -	-
221	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	255.23	251.39	11/2008 -	-
	Total		1,02,439.53 -	1,19,874.80	1,56,240.10		
	<u>TELECOMMUNICATIONS</u>						
	<u>Department Of Telecommunication</u>						
222	NETWORK FOR SPECTRUM - [N26000101	3/2012	13,334.00 -	24,664.00	17,845.00	07/2015 -	07/2021
	Total		13,334.00 -	24,664.00	17,845.00		
	<u>URBAN DEVELOPMENT</u>						
	<u>Chennai Metro Rail Ltd</u>						
223	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084	2/2009	14,600.00 -	19,058.00	16,365.87	12/2015 -	-
	<u>Delhi Metro Rail Corporation</u>						
224	DELHI MRTS PHASE-III - [N28000056	9/2011	38,585.00 -	38,585.00	39,182.53	03/2016 -	09/2021
	<u>Kochi Metro Rail Corporation Ltd</u>						
225	KOCHI METRO RAIL PROJECT - [N28000081	7/2012	5,181.79 -	6,218.14	6,059.17	07/2017 -	09/2020
	<u>National Building Construcion Corporation Ltd</u>						
226	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080	6/2012	4,264.00 -	4,720.73	4,683.08	11/2019 -	-
	Total		62,630.79 -	68,581.87	66,290.65		

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>WATER RESOURCES</u>						
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>						
227	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037	12/2014	225.77 -	225.77	276.57	03/2020 -	03/2021
228	SAIDPUR SEWER NETWORK PATNA - [N30000039	4/2015	268.63 -	268.63	296.97	01/2021 -	-
	Total		494.40 -	494.40	573.54		
	Grand Total		3,14,915.45	4,86,474.55	4,64,634.59		

Details of Delayed Projects w.r.t. Original Schedule

Annexure - VI

Costing Rs. 150 Crore and above (April 2021)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
	<u>Bhavini Limited</u>									
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [N02100044]BHAVNI, TAMIL NADU	09/2003	3,492.00 5,677.00	6,840.00	5,935.96	09/2010 09/2016	10/2022	145	95.88	
	<u>Nuclear Power Corporation Of India Limited</u>									
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 -	16,580.00	16,488.00	12/2015 -	02/2022	74	44.69	
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 -	17,079.00	13,206.00	12/2016 -	03/2023	75	38.63	
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL, TAMIL NADU	03/2013	39,849.00 -	39,849.00	23,925.00	11/2020 -	11/2023	36	0	
	Total		67,120.00 -	80,348.00	59,554.96					
	<u>CIVIL AVIATION</u>									
	<u>Airport Authority Of India Limited</u>									
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, A & N ISLANDS	10/2013	417.23 707.73	707.73	379.95	09/2018 09/2020	06/2021	33	69.63	NIL
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI, TRIPURA	09/2015	438.28 -	402.00	366.61	06/2019 12/2020	06/2021	24	-8.28	NIL
7	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA - [N04000080]AAI, WEST BENGAL	01/2016	458.00 -	458.00	135.60	03/2020 12/2021	12/2021	21	0	
8	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN - [N04000085]AAI, UTTARAKHAND	07/2018	456.86 -	456.86	286.85	09/2020 -	12/2021	15	0	NIL
9	UPGRADATION OF JABALPUR AIRPORT - [N04000087]AAI, MADHYA PRADESH	06/2016	412.24 -	412.24	195.70	06/2021 -	12/2021	6	0	Diversion of Road Crossing the runway is pending with state Govt. (Amount Deposited by AAI)

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
10	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT - [N04000089]AAI,ANDHRA PRADESH	08/2017	177.10 -	177.10	86.01	02/2020 06/2021	12/2021	22	0	1. A portion of the site measuring 3.42 acres is fouling in the Runway extension and Basic Strip due to which the work will be further delay 2. High mast transmission towers in the approach path of Runway 08 to be shifted by APTRANSCO (Govt. of AP undertaking) for final commissioning of the Project and this part of the work is yet to physically start. However work order is placed by State Government and agency mobilizing Men,materials & Machinery for the work.
11	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076]AAI,DELHI	11/2016	303.80 351.21	303.80	167.55	04/2020 -	03/2022	23	0	NIL
12	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]AAI,ASSAM	12/2016	1,142.00 -	1,232.00	368.37	03/2021 03/2022	03/2022	12	7.88	Transportation strike from 1st week of November 2020, to end of the month at CEMENT Plant in Govt, of Assam & Meghalaya.
13	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]AAI,TAMIL NADU	08/2018	951.28 -	951.28	408.94	10/2021 -	07/2022	9	0	NIL
14	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI - [N04000074]AAI,TAMIL NADU	06/2018	2,467.00 -	2,467.00	608.22	02/2022 -	08/2022	6	0	NIL
15	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]AAI,UTTAR PRADESH	06/2018	1,383.00 -	1,383.00	369.66	09/2021 -	09/2022	12	0	
16	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA - [N04000081]AAI,WEST BENGAL	01/2019	389.71 -	389.71	140.62	11/2021 10/2022	10/2022	11	0	
17	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082]AAI,BIHAR	05/2018	1,216.90 -	1,216.90	205.04	10/2022 -	03/2023	5	0	Vacation of RCC Hangar of State Govt. for clearance of Terminal Building site.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
18	DEVELOPMENT OF TUTICORIN AIRPORT - [N04000090]AAI,TAMIL NADU	06/2019	380.87 -	380.87	5.99	03/2022 03/2022	03/2023	12	0	NIL
	Total		10,594.27 -	10,938.49	3,725.11					
	<u>COAL</u>									
	<u>Bharat Coking Coal Limited</u>									
19	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	289.45	281.33	05/2014 -	07/2021	86	0	
20	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	463.92	04/2015 -	03/2022	83	0	
21	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]BCCL, WEST BENGAL	12/2015	304.13 341.22	341.22	40.84	03/2017 -	03/2022	60	12.2	
22	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]BCCL,JHARKHAND	10/2015	243.00 334.27	334.27	18.35	04/2018 -	06/2022	50	37.56	
23	MURADIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	24.23	04/2014 -	04/2023	108	0	
	<u>Central Coal Fields Limited</u>									
24	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	107.27	03/2011 -	03/2022	132	0	
25	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	426.30	03/2016 -	03/2022	72	0	
26	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	98.21	03/2014 -	03/2022	96	0	
27	RECAST EPR AMRAPALI OC - [N06000103]CCL,JHARKHAND	02/2012	4,983.58 4,983.58	4,983.58	245.85	03/2020 03/2024	03/2024	48	0	
28	MAGADH EXPANSION OC(51 MTY) - [N06000015]CCL,JHARKHAND	08/2008	6,964.33 6,964.33	706.40	706.20	07/2012 03/2025	03/2025	152	-89.86	
	<u>Eastern Coal Fields Limited</u>									
29	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL, WEST BENGAL	08/2012	1,055.05 -	1,055.05	669.82	03/2018 -	10/2021	43	0	1. Rehabilitation of PAFs: Progress of R&R activity delayed due to disputes among villagers for selection of rehab. site and resistance by villagers in shifting. 2. Expediting the work of tree felling for hand over of 32.65 Ha forest land.
30	EXPANSION PR OF JHANJRA UG(5.00 MTY) - [N06000020]ECL, WEST BENGAL	11/2015	1,210.12 -	1,210.12	26.05	03/2022 03/2029	03/2029	84	0	
	<u>Mahanadi Coal Fields Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
31	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.53 -	479.53	475.14	03/2013 -	03/2022	108	0	
32	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL, ODISHA	05/2014	479.15 -	479.15	278.53	03/2019 -	03/2024	60	0	
33	GARJANBAHAL OCP - [N06000117]MCL, ODISHA	11/2014	1,375.38 -	1,375.38	504.36	03/2021 -	03/2024	36	0	
34	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY) - [N06000035]MCL, ODISHA	12/2007	8,416.19 8,416.19	8,416.19	890.78	03/2013 03/2028	03/2028	180	0	
35	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY) - [N06000044]MCL, ODISHA	12/2007	3,504.21 3,504.21	3,504.21	607.83	03/2010 03/2029	03/2029	228	0	
36	BHUBANESWARI EXPENSION OCP(40.0 MTY) - [N06000034]MCL, ODISHA	12/2007	3,145.45 -	3,145.45	612.55	03/2017 -	03/2031	168	0	
	<u>Neyveli Lignite Corporation</u>									
37	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC, UTTAR PRADESH	07/2016	17,237.00 -	17,237.80	11,574.21	11/2021 07/2022	07/2022	8	0	
38	PACHWARA SOUTH COAL BLOCK - [N06000193]NLC, JHARKHAND	07/2013	1,795.01 -	1,795.01	34.88	08/2022 -	09/2023	13	0	
39	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC, TAMIL NADU	04/2013	1,458.17 709.06	709.06	484.81	06/2015 03/2025	03/2025	117	-51.37	
	<u>Northern Coal Fields Limited</u>									
40	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL, MADHYA PRADESH	05/2017	1,783.09 -	1,783.09	622.66	03/2021 -	03/2022	12	0	
41	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]NCL, MADHYA PRADESH	11/2017	1,255.17 -	1,255.17	152.16	03/2022 -	03/2023	12	0	
	<u>Singareni Colliers Company Limited</u>									
42	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29 -	164.04	129.58	03/2015 -	03/2022	84	-32.3	
43	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL, TELANGANA	07/2011	162.76 -	349.28	251.14	03/2015 -	03/2022	84	114.6	
44	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL, TELANGANA	07/2012	417.33 -	384.32	131.62	07/2016 -	03/2022	68	-7.91	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
45	KAKATIYAKHANI OPENCAS-2 PROJECT - [N06000129]SCCL,TELANGANA	05/2015	397.09 -	442.42	109.25	03/2019 -	03/2022	36	11.42	
46	KAKATIYAKHANI OPENCAS III PROJECT PHASE-1 - [N06000161]SCCL,TELANGANA	03/2017	413.84 -	413.84	230.95	03/2019 -	03/2022	36	0	
47	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	489.62	416.07	03/2012 -	03/2023	132	16.86	
48	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	473.22	79.04	03/2015 -	03/2023	96	5.85	
	<u>South-Eastern Coal Fields Limited</u>									
49	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH	09/2008	152.43 459.49	459.49	202.90	03/2015 03/2020	03/2022	84	201.44	
50	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	6.50	03/2014 -	03/2022	96	0	
51	AMADAND OPENCAS EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH	03/2016	869.44 -	869.44	123.17	03/2021 -	03/2022	12	0	
52	AMERA OC RCE - [N06000123]SECL,CHHATISGARH	02/2015	335.97 -	335.97	49.49	03/2018 -	03/2023	60	0	
53	AMGAON OPENCAS PROJECT RCE - [N06000135]SECL,CHHATISGARH	07/2015	316.10 -	316.10	141.02	03/2020 -	03/2023	36	0	
54	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH	12/2014	371.04 -	371.04	77.27	03/2021 -	03/2024	36	0	
55	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH	12/2014	357.80 -	357.80	100.63	03/2021 04/2024	04/2024	37	0	
56	DURGAPUR OPENCAS PROJECT - [N06000136]SECL,CHHATISGARH	02/2015	916.24 -	916.24	11.38	03/2023 -	03/2026	36	0	
	<u>Western Coal Fields Limited</u>									
57	SINGHORI OC MINE - [N06000130]WCL,MAHARASHTRA	06/2015	205.49 -	205.49	138.12	03/2020 -	09/2021	18	0	
58	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL,MAHARASHTRA	02/2016	198.68 -	325.18	253.17	03/2019 -	03/2022	36	63.67	
59	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL,MAHARASHTRA	03/2017	362.73 -	402.90	330.34	03/2020 -	09/2022	30	11.07	
60	UKNI DEEP OC - [N06000179]WCL,MAHARASHTRA	11/2018	318.14 -	318.14	211.41	03/2021 -	09/2022	18	0	
61	BELLORA-NAIGAON DEEP OC - [N06000180]WCL,MAHARASHTRA	11/2018	252.71 -	252.71	101.09	03/2021 -	09/2022	18	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
62	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL,MULTI STATE	02/2017	328.00 -	328.00	295.83	03/2021 -	09/2023	30	0	
63	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA	08/2015	288.90 -	333.43	142.27	03/2023 -	03/2024	12	15.41	
64	REVISED PR FOR AMALGAMATED INDER KAMPTEE DEEP OC (3.2 MTY) - [N06000141]WCL,MAHARASHTRA	11/2015	313.34 -	313.34	148.72	03/2021 -	03/2024	36	0	
65	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]WCL,MULTI STATE	09/2016	289.29 -	289.30	35.95	03/2022 -	03/2025	36	0	
66	RPR FOR MUNGOLI NIORGUDA EXTENSION (DEEP) OC (4.375 MTY) - [N06000142]WCL,MAHARASHTRA	11/2015	851.60 -	826.80	230.50	03/2020 -	03/2026	72	-2.91	
67	RPR FOR JAMUNIA UG (0.90 MTY) - [N06000153]WCL,MADHYA PRADESH	07/2016	281.25 -	281.25	21.35	03/2022 -	03/2026	48	0	
68	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA	05/2015	295.56 -	496.38	164.25	03/2019 -	09/2026	90	67.95	
69	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA	02/2016	304.52 -	729.86	160.67	03/2019 -	09/2026	90	139.68	
70	PR FOR DINESH(MAKARDHOKRA III) EXPANSION OC (8.0 MTY) - [N06000118]WCL,MAHARASHTRA	11/2014	1,184.33 -	1,184.33	383.13	03/2020 -	03/2027	84	0	
	Total		69,856.32 -	64,315.47	24,023.09					
	<u>FINANCE</u>									
	<u>Central Public Works Department</u>									
71	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD,TAMIL NADU	12/2015	209.00 -	208.96	205.72	10/2019 -	07/2021	21	-0.2	
	Total		209.00 -	208.96	205.72					
	<u>FERTILISERS</u>									
	<u>National Fertiliser Limited</u>									
72	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]NFL,PUNJAB	01/2018	218.83 -	218.83	191.30	11/2019 05/2021	04/2021	17	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
73	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]NFL,PUNJAB	01/2018	239.81 -	239.81	199.11	11/2019 05/2021	04/2021	17	0	
74	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]NFL,HARYANA	01/2018	215.92 -	215.92	168.30	11/2019 06/2021	05/2021	18	0	
	<u>Rashtriya Chemical & Fertiliser Limited</u>									
75	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]RCF,MAHARASHTRA	04/2018	426.72 -	426.72	288.80	04/2020 03/2021	07/2021	15	0	
	Total		1,101.28 -	1,101.28	847.51					
	<u>MINES</u>									
	<u>National Aluminum Company Limited (Nalco)</u>									
76	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]NALCO,ODISHA	12/2014	5,540.00 6,435.90	5,540.00	731.55	04/2021 12/2022	12/2022	20	0	
77	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]NALCO,ODISHA	11/2017	483.00 483.00	483.00	.92	04/2021 03/2023	03/2023	23	0	
	Total		6,023.00 -	6,023.00	732.47					
	<u>STEEL</u>									
	<u>National Mineral Development Corporation (Nmdc)</u>									
78	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH	01/2010	15,525.00 21,940.00	21,940.00	18,516.49	05/2015 07/2021	07/2021	74	41.32	
	<u>Rastriya Ispat Nigam Limited</u>									
79	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH	04/2014	1,682.85 -	1,682.85	1,564.62	09/2018 06/2021	06/2021	33	0	No

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
80	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH	12/2011	2,858.00 -	2,558.00	1,838.96	12/2017 12/2021	12/2021	48	-10.5	No
	<u>Steel Authority Of India Limited (SAIL)</u>									
81	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND	11/2016	262.87 -	262.87	185.85	06/2019 05/2021	08/2021	26	0	
82	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E - [N12000121]SAIL,WEST BENGAL	12/2018	263.36 -	263.36	215.38	09/2020 03/2021	09/2021	12	0	
83	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	1,034.01	537.82	10/2017 12/2021	12/2021	50	0	
	Total		21,626.09 -	27,741.09	22,859.12					
	<u>PETROLEUM</u>									
	<u>Bharat Petroleum Corporation Limited</u>									
84	MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL,MAHARASHTRA	04/2013	449.58 -	449.58	396.13	12/2019 04/2021	04/2021	16	0	
85	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA	11/2014	4,588.29 5,245.96	5,245.96	5,076.00	08/2018 11/2019	05/2021	33	14.33	
86	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA	02/2016	3,313.00 -	3,288.96	2,967.01	02/2020 03/2021	05/2021	15	-7.3	
87	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]BPCL,KARNATAKA	10/2018	206.26 -	206.26	132.84	03/2021 -	05/2021	2	0	
88	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA	12/2015	1,112.00 1,507.24	1,507.24	730.00	06/2019 -	02/2022	32	35.54	
89	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 1,472.00	1,472.00	19.44	02/2017 08/2022	08/2022	66	117.11	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
90	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364]BPCL, ANDHRA PRADESH	07/2017	580.20 -	580.20	155.84	02/2021 -	03/2023	25	0	
	<u>Chennai Petroleum Corporation Limited</u>									
91	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL, TAMIL NADU	08/2017	421.00 -	300.00	241.01	08/2020 -	09/2021	13	-28.74	
	<u>Gas Authority Of India Limited</u>									
92	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL, GUJARAT	04/2016	327.78 -	200.00	196.50	04/2018 -	06/2021	38	-38.98	
93	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]GAIL, MULTI STATE	03/2017	2,433.00 -	2,433.00	2,110.70	12/2020 12/2021	06/2021	6	0	
94	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]GAIL, HARYANA	08/2018	286.42 327.01	327.01	186.00	08/2020 05/2021	06/2021	10	14.17	
95	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL, MULTI STATE	07/2015	2,881.40 -	2,000.00	1,607.70	12/2020 -	09/2021	9	-30.59	
96	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT - [N16000390]GAIL, UTTAR PRADESH	08/2018	217.92 217.92	217.92	89.80	04/2021 -	10/2021	6	0	
97	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]GAIL, ODISHA	03/2017	1,933.00 -	1,933.00	1,268.75	12/2020 12/2021	12/2021	12	0	
98	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]GAIL, MULTI STATE	03/2017	3,437.00 3,048.00	3,048.00	1,852.90	12/2020 12/2021	12/2021	12	-11.32	
99	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]GAIL, WEST BENGAL	03/2017	1,740.00 -	1,740.00	764.50	12/2020 12/2021	12/2021	12	0	
100	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]GAIL, GUJARAT	09/2018	225.54 247.90	247.90	40.10	02/2021 -	12/2021	10	9.91	
101	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL, MULTI STATE	06/2009	2,915.00 5,909.00	5,909.00	3,607.20	12/2012 02/2022	02/2022	110	102.71	
	<u>Hindustan Petroleum Corporation Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
102	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]HPCL,HARYANA	11/2017	255.00 300.00	300.00	271.70	11/2020 06/2021	06/2021	7	17.65	
103	SWRO II WITH LLPH FACILITIES - [N16000378]HPCL,ANDHRA PRADESH	09/2019	196.26 -	196.26	92.38	07/2020 -	07/2021	12	0	
104	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA	06/2017	249.26 -	249.26	134.44	06/2020 12/2021	09/2021	15	0	
105	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]HPCL,JHARKHAND	06/2017	161.50 -	161.50	78.18	06/2020 09/2021	09/2021	15	0	
106	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH	07/2016	20,928.00 26,264.00	26,264.00	14,820.38	07/2020 07/2022	07/2022	24	25.5	
107	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSP) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]HPCL,MULTI STATE	09/2017	2,677.00 -	3,072.00	2,239.96	06/2021 08/2022	08/2022	14	14.76	
108	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS - [N16000385]HPCL,HARYANA	09/2018	520.00 -	520.00	126.72	09/2026 02/2027	02/2027	5	0	
109	CITY GAS DISTRIBUTION IN UP AND UK - [N16000387]HPCL,UTTAR PRADESH	03/2019	3,450.20 -	3,450.20	235.43	03/2029 08/2029	08/2029	5	0	
	<u>Indian Oil Corporation Limited</u>									
110	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	545.44	07/2018 05/2021	05/2021	34	0	
111	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR), CACHAR, ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM	06/2016	423.00 -	502.00	422.12	08/2019 06/2021	06/2021	22	18.68	
112	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND	02/2017	160.10 -	160.10	93.54	02/2020 06/2021	06/2021	16	0	
113	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]IOCL,BIHAR	07/2018	189.00 -	189.00	149.34	01/2021 06/2021	06/2021	5	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
114	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]IOCL,ASSAM	08/2018	557.00 -	557.00	496.45	02/2020 06/2021	06/2021	16	0	
115	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]IOCL,HARYANA	04/2018	206.63 -	206.63	93.11	02/2020 08/2021	08/2021	18	0	
116	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00 -	212.00	148.29	01/2021 -	09/2021	8	0	
117	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL,MAHARASHTRA	05/2016	261.00 -	261.00	158.24	01/2021 -	09/2021	8	0	
118	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]IOCL,MADHYA PRADESH	08/2017	236.00 293.00	293.00	161.05	06/2020 09/2021	09/2021	15	24.15	
119	LPG BP PROJECT MOTIHARI - [N16000317]IOCL,BIHAR	05/2018	206.50 -	206.50	134.97	03/2021 09/2021	09/2021	6	0	
120	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 -	348.00	217.55	01/2021 -	10/2021	9	0	
121	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL, WEST BENGAL	04/2017	163.02 -	163.02	101.52	04/2020 10/2021	10/2021	18	0	
122	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT	10/2017	906.00 -	906.00	279.82	02/2020 10/2021	10/2021	20	0	
123	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	318.80	147.52	08/2021 -	11/2021	3	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
124	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]IOCL,UTTAR PRADESH	08/2017	255.40 -	255.40	64.34	08/2020 11/2021	11/2021	15	0	
125	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 3,027.90	3,027.90	1,957.55	03/2021 12/2021	12/2021	9	66.09	
126	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH	08/2018	466.00 -	466.00	256.49	04/2021 12/2021	12/2021	8	0	
127	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]IOCL,BIHAR	04/2018	522.00 -	522.00	323.87	03/2021 12/2021	12/2021	9	0	
128	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	466.43	207.05	10/2020 01/2022	01/2022	15	0	
129	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU	05/2016	4,497.00 6,025.00	6,025.00	3,681.97	12/2018 02/2022	02/2022	38	33.98	
130	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]IOCL,HARYANA	10/2018	598.00 -	598.00	293.80	02/2020 02/2022	02/2022	24	0	
131	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	10/2015	607.06 1,236.00	1,236.00	394.74	10/2017 03/2022	03/2022	53	103.6	
132	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00 3,338.00	3,338.00	2,923.70	12/2020 03/2022	03/2022	15	43.82	
133	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA	12/2016	161.59 -	161.59	49.59	12/2019 03/2022	03/2022	27	0	
134	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]IOCL,ODISHA	10/2018	1,297.50 -	1,297.50	722.93	10/2021 -	03/2022	5	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
135	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]IOCL,ANDHRA PRADESH	10/2018	316.20 -	316.20	98.14	10/2021 03/2022	03/2022	5	0	
136	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]IOCL,HARYANA	01/2019	909.00 -	909.00	309.94	01/2021 03/2022	03/2022	14	0	
137	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383]IOCL,HARYANA	09/2019	164.69 -	164.69	13.16	07/2021 03/2022	03/2022	8	0	
138	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]IOCL,HARYANA	08/2018	1,636.00 -	1,636.00	723.59	08/2020 04/2022	04/2022	20	0	
139	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]IOCL,ODISHA	11/2018	462.30 -	462.30	23.19	09/2021 06/2022	06/2022	9	0	
140	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT - [N16000363]IOCL,HARYANA	12/2018	278.60 -	278.60	44.73	06/2021 07/2022	07/2022	13	0	
141	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]IOCL,BIHAR	12/2017	199.36 -	199.36	34.40	10/2020 08/2022	08/2022	22	0	
142	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]IOCL,ODISHA	05/2019	3,361.00 -	3,361.00	1,665.03	08/2021 09/2022	09/2022	13	0	
143	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	355.00	106.53	04/2022 -	02/2023	10	0	
144	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]IOCL,ODISHA	06/2019	371.00 -	371.00	4.44	09/2022 03/2023	03/2023	6	0	
145	R and D CAMPUS II AT FARIDABAD - [N16000375]IOCL,HARYANA	06/2019	2,281.94 -	2,281.94	431.31	12/2022 07/2023	07/2023	7	0	
146	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA	12/2018	611.00 -	611.00	76.47	04/2022 -	08/2023	16	0	
	<u>Mangalore Refinery And Petrochemicals Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
147	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA	11/2017	581.00 637.00	637.00	489.10	03/2020 11/2020	07/2021	16	9.64	
148	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA	09/2016	1,810.00 1,810.00	1,810.00	1,658.31	12/2019 04/2021	02/2022	26	0	
	<u>Oil & Natural Gas Corporation Limited</u>									
149	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]ONGC,ASSAM	07/2016	249.85 303.75	303.75	199.31	05/2020 05/2021	05/2021	12	21.57	
150	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]ONGC,MAHARASHTRA	05/2019	763.92 -	733.86	757.62	12/2020 05/2021	05/2021	5	-3.93	
151	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	650.82 -	624.35	447.05	03/2019 09/2021	09/2021	30	-4.07	
152	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]ONGC,MAHARASHTRA	02/2019	2,292.46 -	2,203.71	1,757.87	05/2021 12/2021	12/2021	7	-3.87	
153	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]ONGC,MAHARASHTRA	05/2019	3,660.71 3,740.05	3,740.05	2,808.52	05/2021 01/2022	01/2022	8	2.17	
154	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 1,846.46	2,001.00	1,551.48	05/2013 02/2022	02/2022	105	132.19	
155	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA	12/2015	3,190.69 3,375.90	3,375.90	2,786.78	04/2018 05/2022	05/2022	49	5.8	
156	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH	03/2016	34,012.00 -	25,090.00	11,254.33	06/2020 06/2022	06/2022	24	-26.23	
157	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]ONGC,MAHARASHTRA	04/2019	3,228.80 3,976.67	3,976.67	1,188.33	03/2022 05/2023	05/2023	14	23.16	
	<u>Oil India Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
158	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL, ASSAM	01/2018	543.91 -	652.10	320.30	02/2020 -	06/2021	16	19.89	
159	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN - [N16000356]OIL, ASSAM	06/2016	224.75 -	222.21	166.48	08/2020 -	06/2021	10	-1.13	
160	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI- BONGAIGAON SECTOR PHASE II - [N16000259]OIL, MULTI STATE	09/2016	571.66 -	571.66	471.81	12/2019 -	08/2021	20	0	
161	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL, MULTI STATE	05/2016	406.00 -	406.00	225.67	10/2020 -	03/2022	17	0	
	Total		1,38,069.09 -	1,45,020.47	83,080.49					
	<u>POWER</u>									
	<u>Central Public Works Department</u>									
162	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD, DELHI	10/2017	271.90 -	271.90	240.96	11/2019 -	06/2021	19	0	
	<u>Chenab Valley Power Projects [P] Limited</u>									
163	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL, JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	1,766.91	04/2020 -	07/2025	63	0	
	<u>National Hydro-Electric Power Corporation</u>									
164	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC, HIMACHAL PRADESH	09/2002	3,919.59 9,897.59	9,897.59	8,945.10	09/2009 07/2022	07/2022	154	152.52	
165	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC, ARUNACHAL PRADESH	09/2003	6,285.33 19,992.43	19,992.43	13,732.39	09/2010 08/2023	08/2023	155	218.08	
	<u>National Thermal Power Corporation</u>									
166	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000274]NTPC, UTTAR PRADESH	03/2019	349.00 -	349.00	226.00	11/2020 -	04/2021	5	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
167	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC, ODISHA	02/2014	12,532.44 13,140.91	13,140.91	11,730.23	12/2018 05/2021	05/2021	29	4.86	Support of State Govt. of Odisha is required for following: •Balance RoW for 132 kV transmission line for Make Up Water pump house.
168	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC, BIHAR	01/2007	5,353.00 10,566.00	10,566.00	8,847.06	07/2012 06/2020	07/2021	108	97.38	Support of State Govt. required for early resolution of acquisition / possession of 42.4355 Acres of critical land balance due to court cases, wrong payments in awarded land and ownership disputes in following areas: Main Plant: 21.372 acres Make-Up water corridor: 0.190 acres Ash Dyke: 14.8135 acres Township: 6.05 acres De-notification of 17.69 Acres GMM land for Raiyatikaran is critical as construction of Overflow Lagoon of Ash Dyke is held up. The proposal for de-notification is with Revenue Dept. GOB, since 05.02.2020. Report sent by Dist Authorities on 15.12.20.
169	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC, ODISHA	05/2016	1,885.13 -	1,885.13	1,763.69	12/2018 -	07/2021	31	0	
170	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC, WEST BENGAL	12/2016	529.68 -	529.68	418.49	11/2018 -	07/2021	32	0	
171	KAYAMKULAM SOLAR 70 MW - [N18000288]NTPC, KERALA	09/2019	403.62 -	403.62	53.13	06/2021 10/2021	10/2021	4	0	
172	NGGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC, BIHAR	01/2013	12,964.60 17,304.00	17,304.00	15,787.92	05/2018 -	12/2021	43	33.47	
173	DEVIKOT SOLAR 90MW - [N18000280]NTPC, UTTAR PRADESH	03/2020	501.29 -	501.29	118.11	09/2021 01/2022	01/2022	4	0	
174	DEVIKOT SOLAR 150MW - [N18000281]NTPC, UTTAR PRADESH	01/2020	798.24 -	798.24	34.64	09/2021 01/2022	01/2022	4	0	
175	NOKHRA - [N18000282]NTPC, UTTAR PRADESH	03/2020	1,722.14 -	1,722.14	132.85	09/2021 01/2022	01/2022	4	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
176	SAMBHU KI BHURJ SOLAR 250 MW - [N18000285]NTPC,RAJASTHAN	01/2020	1,522.71 -	1,522.71	437.60	09/2021 01/2022	01/2022	4	0	
177	SAMBHU KI BHURJ-II SOLAR 300MW - [N18000286]NTPC,RAJASTHAN	03/2020	1,782.00 -	1,782.00	200.75	09/2021 01/2022	01/2022	4	0	
178	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA	01/2016	10,598.98 10,997.70	10,997.70	8,368.64	11/2020 07/2022	07/2022	20	3.76	
179	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 -	15,389.42	11,722.10	06/2019 10/2022	10/2022	40	7.12	Support of State Govt of Jharkhand is required for following: 1.Maintaining Law & order and resolution of following issue: An agitation is going on by "Visthapit Vikas Sangarsh Samiti", demanding additional compensation for already acquired land. Work is completely stopped since 23.02.21 as the labor has been forced to leave the Site by agitators. 2.Acquisition / transfer/ possession of balance land for Ash Dyke and Reservoir. 3.Acquisition of Land by CCL for external CHP. 4.Early completion of Road Widening and strengthening of SH-7 from Hazaribagh to Bijupara. It is being done on deposit basis by RCD. The road diversion in project area needs to be completed on priority. 5.Repair of damaged bridge over Garhi River is critical for transportation of material for project. 6.Forest clearance in ATS lines.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
180	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 5,867.38	5,867.38	4,913.02	03/2013 12/2021	12/2022	117	96.99	Award of Srinagar to Kashipur transmission line by PTCUL for power evacuation. Support of State Govt. of Uttarakhand is required for expeditious completion of Transmission line for Power evacuation system. During the meeting held on 16.10.2020 headed by Chairman CEA along PTCUL and NTPC, CEA and NTPC expressed its concern regarding delay in award of critical Srinagar to Kashipur line by PTCUL. It was decided that CEA would request PSPA-I Division, CEA to examine the proposal of PTCUL for construction of Khandulkhal- Koteswar 400kV line, instead of Srinagar (Khandulkhal) – Kashipur (Ranpura) 400 kV D/C line so that the line could be constructed before Jun'22. Also CEA had another meeting with NTPC, PTCUL, CTU and NRLDC on 09.11.20. regarding readiness of Power Evacuation System for TVHPP.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(April 2021)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
181	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 21,312.11	21,312.11	18,595.56	10/2011 07/2023	07/2023	141	145.16	•Support required for early completion of Hazaribagh-Koderma-Tilaiya-Rajgir-Bakhtiyarpur rail route, which is critical to ease transportation of coal for Barh Project. Readiness of railway line Hazaribagh-Koderma-Tilaiya-Rajgir-Bakhtiyarpur route (250km) is critical to ease transportation of coal for Barh Project. NTPC has funded Rs 664 Crores to Railways for development of following works in envisaged Coal transportation route. • Construction of Karnauti-Bakhtiyarpur flyover. • Construction of Manpur Flyover (ROR) • Electrification of Manpur-Tilaiya-Bakhtiyarpur section. (Charging from Tilaiya sub-station balance) Bakhtiyarpur ROR line: Acquisition of 12.241 Acres supplementary land is under process. Land award has been done. Payment to landowner is in progress. However, few Raiyats are unwilling to accept the compensation as the award has been issued based on reduced circle rate. State Govt support required to Railways for acquisition / possession of said Land. Support of Ministry of Railways is required for timely completion of above works.
182	PATRATU STPP-I (3X800MW) - [N18000275]NTPC,JHARKHAND	11/2017	18,668.00 -	17,112.00	4,351.86	03/2023 -	09/2024	18	-8.34	Support requested for resolving inter-ministerial issues.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
183	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC, WEST BENGAL	09/2014	1,381.84 -	1,381.54	668.04	09/2019 12/2024	12/2024	63	-0.2	•All inputs as regards to signing of PPA provided to West Bengal Electricity Corporation Limited. WBSECL to take board approval for further submission of proposal to WBSECL. State Govt is not ready to finalize power evacuation line in absence of PPA. •Shifting of balance Homesteads from Project area. (11Nos + 01 School).
	<u>Power Grid Corporation Of India Limited</u>									
184	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL, MULTI STATE	03/2016	808.63 -	808.63	662.19	01/2018 04/2021	05/2021	40	0	
185	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL, WEST BENGAL	04/2016	454.11 -	454.11	343.81	04/2018 03/2021	05/2021	37	0	
186	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL, MULTI STATE	11/2017	358.83 -	358.83	253.49	05/2020 05/2021	05/2021	12	0	
187	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL, MULTI STATE	01/2014	374.63 -	374.63	246.80	04/2016 12/2017	06/2021	62	0	
188	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL, MULTI STATE	05/2014	522.29 546.36	546.36	478.29	11/2016 09/2021	06/2021	55	4.61	
189	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL, MULTI STATE	03/2015	197.40 -	197.40	90.05	03/2018 -	06/2021	39	0	
190	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL, MULTI STATE	05/2016	14,733.37 -	14,733.37	11,552.37	11/2019 04/2021	06/2021	19	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
191	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	235.53	151.12	06/2019 08/2021	06/2021	24	0	
192	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL,MULTI STATE	02/2017	5,070.13 -	5,070.13	4,101.57	04/2020 06/2021	06/2021	14	0	
193	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE	03/2017	3,500.00 3,500.00	3,994.00	2,917.31	07/2020 12/2020	06/2021	11	14.11	
194	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 219.66	219.66	157.20	07/2019 04/2021	06/2021	23	17.99	
195	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE	08/2017	1,931.39 -	1,931.39	1,709.25	02/2020 06/2021	06/2021	16	0	
196	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	1,394.52	534.89	05/2017 09/2021	09/2021	52	0	
197	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE	02/2017	322.30 -	322.30	201.55	02/2019 06/2021	09/2021	31	0	
198	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE	03/2017	379.95 -	379.95	232.02	12/2019 06/2021	09/2021	21	0	
199	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 6,700.00	6,700.00	2,767.14	12/2018 -	12/2021	36	31.08	
200	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 14,719.10	14,719.10	12,894.95	08/2013 08/2022	08/2022	108	32.24	
201	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 9,129.32	9,129.32	2,163.30	12/2018 -	03/2024	63	92.02	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>Thdc India Limited</u>									
202	AMELIA COAL MINE - [N18000252]THDCIL,MADHYA PRADESH	01/2017	2,104.21	1,587.16	495.58	09/2020 08/2022	08/2022	23	-24.57	1. Te nancy/Private land (337.35 Ha): 23 out of 53 cases involving about 400 land losers pending in Court of Collector, Singrauli due to which distribution of Compensation is delayed. 2. Go vt. land for R&R (53.13 Ha): Declaration of the land as "Abadi Land" is pending at GoMP. 3. Govt. land of Coal Block (178.13 Ha): Collector, Singrauli informed that permission under section 247 shall be accorded after grant of Mining Lease which is pending with Director (Mining), GoMP.
203	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58	3,860.35	2,223.06	06/2013	12/2023	126	54.94	Permission for Mining at Gadi Quarry from GoUK La nd of 4.292 Ha. Of Gadi quarry has been designated for the construction works of Power House and HRT of the project from where continuous supply of aggregate is to be made available for the works. Go UK vide letter dated 19.04.21 to DM, Chamoli has issued Mining permission to the project. Th ereafter, process for lease deed, demarcation of mining land, etc has been initiated.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
204	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH	03/2019	11,089.42 -	11,089.42	1,767.11	09/2023 -	08/2024	11	0	- Continuous help of District administration is required for expeditious land acquisition. - Continuous help of District administration is required for expeditious shifting of Nagla residents to newly identified land.
	Total		1,82,770.04 -	2,38,945.07	1,58,998.10					
	<u>HEALTH AND FAMILY WELFARE</u>									
	<u>Central Public Works Department</u>									
205	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA	10/2016	209.84 -	209.84	136.48	03/2020 -	05/2021	14	0	
206	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST - [N28000112]CPWD,KERALA	09/2017	150.29 -	150.29	43.43	03/2020 -	12/2021	21	0	
207	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT - [N28000139]CPWD,PONDICHERRY	03/2018	195.00 -	195.00	16.41	09/2020 -	04/2022	19	0	
208	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD,HIMACHAL PRADESH	12/2018	260.00 -	260.00	25.38	06/2021 -	05/2022	11	0	
	<u>HII Infra Tech Services Limited</u>									
209	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	715.06	548.39	04/2020 -	07/2021	15	-8.91	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
210	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	557.48	469.13	06/2020 -	07/2021	13	-20.7	
211	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 -	747.80	331.55	05/2021 -	07/2022	14	-14.54	
	<u>Hospital Services Consultancy Corporation Ltd</u>									
212	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	499.23	494.72	11/2013 -	05/2021	90	20.55	
213	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC, WEST BENGAL	08/2017	355.15 -	355.15	298.76	03/2019 -	06/2021	27	0	
214	NEIGRIHMS SHILLONG MEGHALAYA - [N21000013]HSCC, MEGHALAYA	10/2016	363.99 -	363.99	239.89	05/2018 -	12/2021	43	0	
	Total		4,311.38 -	4,053.84	2,604.14					
	<u>RAILWAYS</u>									
	<u>Central Railways</u>									
215	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR, MAHARASHTRA	02/1997	2,271.50 -	4,517.49	2,648.51	03/2021 -	03/2023	24	98.88	
216	KALYAN-KASARA 3RD LINE - [N22000233]CR, MAHARASHTRA	04/2011	792.89 -	1,377.48	335.23	03/2021 -	03/2023	24	73.73	
217	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR, MAHARASHTRA	02/2015	1,272.19 -	1,283.49	408.70	03/2022 -	03/2023	12	.89	
218	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR, MAHARASHTRA	04/2012	540.02 -	540.02	272.55	03/2022 -	03/2024	24	0	
219	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR, MAHARASHTRA	02/2015	2,449.91 -	2,449.91	332.19	03/2023 -	03/2024	12	0	
220	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR, MAHARASHTRA	02/2016	1,035.16 -	1,035.16	244.12	03/2022 -	03/2024	24	0	
221	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR, MAHARASHTRA	02/2016	637.95 -	637.95	182.65	03/2023 -	03/2024	12	0	
	<u>East Central Railways</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
222	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	678.54 678.54	929.86	848.39	03/2019 -	05/2021	26	37.04	
223	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	477.88 283.95	751.55	694.88	03/2012 -	07/2021	112	57.27	
224	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	528.57	179.78	03/2019 -	03/2022	36	0	
225	GARHWA ROAD-RAMNA - [N22000465]ECR,JHARKHAND	03/2015	348.23 -	348.23	336.32	03/2021 -	03/2022	12	0	
226	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 -	1,185.73	217.95	03/2021 -	06/2022	15	62.06	
227	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	324.73 -	1,070.00	1,069.58	03/2012 -	11/2022	128	229.5	
228	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	548.00 -	819.01	535.44	03/2020 -	03/2023	36	49.45	
229	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR	12/2015	1,200.20 1,200.20	1,200.20	578.18	03/2020 -	03/2023	36	0	
230	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR	12/2015	1,491.47 -	1,491.47	508.88	03/2020 -	03/2023	36	0	
231	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	1,138.31	03/2020 -	03/2024	48	0	
232	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 -	1,215.54	426.72	03/2021 -	03/2024	36	63.37	
	<u>East Coast Railway</u>									
233	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 -	1,539.28	1,109.06	02/2019 -	12/2021	34	38.43	
234	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 238.03	238.03	221.48	03/2020 03/2021	03/2022	24	52.77	
235	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	1,160.00 1,160.83	1,160.83	950.18	03/2020 03/2023	03/2023	36	.07	
236	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 1,547.38	1,547.38	612.77	03/2022 03/2023	03/2023	12	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
237	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 843.04	843.04	227.52	10/2020 03/2024	03/2024	41	0	
238	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 -	2,499.71	671.08	03/2022 03/2024	03/2024	24	0	
239	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	810.02	171.45	11/2018 -	03/2024	64	15.45	
240	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 1,172.92	1,172.92	613.52	12/2018 03/2024	03/2024	63	0	
241	TALCHER- BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 1,928.07	1,928.07	873.81	06/2021 03/2025	03/2025	45	137.8	
242	KHURDA ROAD- BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 3,791.66	3,791.66	1,506.95	03/2009 03/2026	03/2026	204	29.71	
243	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 2,361.74	2,361.74	432.17	03/2022 03/2026	03/2026	48	0	
	<u>Eastern Railways</u>									
244	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	1,425.44	638.05	02/2013 -	03/2024	133	134.8	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
245	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	1,619.48	905.06	03/2019 12/2009	03/2025	72	36.22	Land Acquisition – 1. Acquisition of land in stretch of 3.30 KM between Kamarpukur and Jairambati is pending for possession to Railway. 2. Villagers of Vill - Bhabadighi, Hooghly District, are not allowing to work over a pond namely Bhabadighi between Goghat and Kamarpukur. 3. Tarakeswar to Dhaniakhali (19 Km) New line, Arambagh – Irphala (18.3 Km) New line, Irphala – Ghatal (11.2 Km) New line and Arambagh – Champadanga (23.30 Km) New line -- Work could not be started due to non - availability of land.
246	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	1,106.62 -	1,091.59	990.33	12/2010 -	03/2025	171	-1.36	Govt. of West Bengal to deposit Rs. 238.75 Cr. for their balance share of cost towards project Katwa-Bardhaman G.C.
247	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER, MULTI STATE	04/1987	406.99 -	545.70	149.31	03/2006 -	03/2025	228	34.08	Land is required for execution of the MM projects.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
248	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	2,137.81	388.53	03/2022 -	03/2025	36	133.39	1. Jharkhand & Bihar Government to expedite land acquisition. Milestones may be set only after physical possession of land. 2. Jharkhand Govt. is to deposit Rs. 168.52 Crs. as share of expenditure incurred in this project upto Sept'2020.
249	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	995.10	645.97	03/2016 -	03/2025	108	7.75	1 Krishnanagar City (Dhubulia) – Charatala (13.00KM) New line, Krishnanagar – Chapra (19.2 KM) New line Work could not be started due to non – availability of land. 2 Krishnanagar – Nabadwipghat (12.2 KM) Gauge Conversion— (Section Krishnanagar – Amghata) could not be commissioned due to 41 nos. of un authorized crossings Amghata to Nabadwipghat work is dropped vide Bd's letter No. 2020/W- I/Compliance in Bd Mtg, dated 09.10.2020
250	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.51 -	769.40	103.86	03/2017 -	03/2025	96	29.2	Suri – Prantik New Line (33.90 km).- The land acquisition details for 250.627 Hectares, submitted to Govt. of West Bengal.
251	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	266.32	191.22	03/2016 -	03/2025	108	-3.95	For Bira - Chakla (11.50) New line- The work will start after acquisition and handing over of land by State Government.
252	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	439.30	411.65	03/2017 -	03/2025	96	20.3	Baruipara – Furfura (12.30 km) New line - Work could not be started due to non-availability of land.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
253	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	494.59	32.00	03/2005 -	03/2025	240	.01	Budge Budge to Pujali (11.00 km) New Line, Pujali – Uluberia (Birshivpur) (10.25 Km) New Line and Pujali – Bahrahat (9.75 Km) New line-- Work could not be started due to non availability of land
254	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96 -	680.68	164.09	02/2012 -	03/2025	157	36.15	Sangrampur – Krishanchandpur (25 Km) New Line, Diamond Harbour (Gurudasnagar) – Bahrahat (21 Km) New Line and Daimond Harbour (Gurudasnagar) - Kulpi (17.25 Km) New Line: Work could not be started due to non availability of land.
255	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	257.42	107.35	03/2014 -	03/2025	132	0	226.542 acres of land required to be acquired for the MM work.
256	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	108	12.02	
	<u>Indian Railway Construction Company Limited</u>									
257	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON,CHHATISGARH	04/2013	3,055.00 -	3,055.15	2,431.72	09/2018 -	03/2022	42	0	
258	GEVRA ROAD PENDRA ROAD - [N22000488]IRCON,CHHATISGARH	02/2014	2,288.00 -	4,970.11	866.16	03/2022 -	12/2023	21	117.23	
259	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA	04/2016	5,200.00 -	962.00	54.75	03/2020 -	03/2024	48	-81.5	
	<u>Metropolitan Rapid Transport Projects</u>									
260	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	63	75.91	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
261	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	734.01	510.69	06/2013 06/2022	12/2021	102	48.06	
262	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 -	2,980.41	1,768.25	03/2004 -	03/2022	216	501.57	
	<u>North Central Railway</u>									
263	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	2,912.96 -	3,845.60	148.26	03/2022 -	12/2024	33	32.02	
	<u>North East Frontier Railway</u>									
264	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	1,180.19 2,531.34	4,541.38	3,804.55	12/2008 -	05/2021	149	284.8	
265	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM	04/2015	870.96 -	1,873.21	1,309.41	03/2021 -	05/2021	2	115.07	
266	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	569.63 -	742.00	200.28	03/2020 -	03/2022	24	30.26	
267	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	385.20 -	1,043.00	837.67	03/2019 -	03/2023	48	170.77	
268	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	2,393.47 5,021.45	5,521.45	3,954.28	03/2014 -	03/2023	108	130.69	
269	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32 -	2,950.00	1,620.12	03/2022 -	03/2023	12	32.15	
270	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	4,454.17 -	12,264.15	10,994.55	03/2011 -	12/2023	153	175.34	
271	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 2,132.03	2,145.00	1,001.65	03/2019 -	03/2024	60	302.54	
272	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 2,042.51	2,042.51	136.41	03/2019 -	03/2024	60	13.6	
273	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52 -	6,911.00	1,204.64	03/2015 -	12/2024	117	197.05	
	<u>North Eastern Railway</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
274	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	1,028.95	172.26	12/2019 -	04/2021	16	-12.65	
275	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	213.35	12.86	04/2016 -	12/2021	68	.16	
276	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	477.31	378.98	01/2019 -	02/2022	37	61.8	
277	AUNRIHAR - JAUNPUR PATCH DOUBLING. - [N22000469]NER,UTTAR PRADESH	04/2016	600.00 -	366.71	117.64	01/2022 -	03/2022	2	-38.88	
278	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	276.90	-	04/2017 -	04/2022	60	0	
279	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	150.00	-	04/2017 -	10/2022	66	0	
280	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH	04/2016	1,900.00 -	1,277.06	-	01/2022 -	03/2025	38	-32.79	
	<u>North Western Railway</u>									
281	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	420.18 -	480.00	357.41	03/2020 -	06/2021	15	14.24	
282	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	860.41	709.62	02/2019 -	06/2022	40	109.82	
283	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	701.81	236.13	03/2020 -	10/2022	31	16.97	
284	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	808.85	232.42	08/2022 -	11/2022	3	0	
	<u>Northern Railway</u>									
285	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	893.45	705.53	12/2011 -	06/2021	114	211.31	
286	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 -	859.00	852.73	03/2016 -	06/2021	63	37.44	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
287	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 -	27,949.00	24,040.61	11/2002 -	12/2022	241	1017.96	
288	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	2,200.00	714.78	07/2012 -	03/2024	140	388.89	
289	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE	04/2007	328.14 1,540.13	1,540.13	242.04	03/2023 03/2025	03/2025	24	369.35	
290	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI - [N22000502]NR,PUNJAB	06/2009	404.00 -	404.00	226.25	08/2016 -	08/2025	108	0	
	<u>Rail India Technical And Economic Service</u>									
291	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498]RITES,CHHATISGARH	02/2016	393.98 -	393.98	350.81	03/2020 -	06/2021	15	0	
	<u>Rail Vikas Nigam Ltd.</u>									
292	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	950.00	810.96	03/2016 -	12/2021	69	50.15	
293	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	713.48 -	2,725.00	2,554.71	03/2020 -	12/2021	21	281.93	
294	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	948.04 -	2,009.00	1,875.48	03/2020 -	12/2021	21	111.91	
295	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	1,402.02 -	1,300.00	1,294.72	03/2020 -	12/2021	21	-7.28	
296	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH	04/2011	1,485.85 -	1,835.83	1,571.35	12/2020 -	12/2021	12	23.55	
297	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,548.66 -	1,868.89	1,831.45	12/2021 -	03/2022	3	20.68	
298	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	3,377.00	2,683.67	03/2020 -	03/2022	24	124.58	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
299	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA	04/1998	1,202.70 -	2,440.53	1,337.54	02/2015 -	06/2022	88	102.92	
300	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL, UTTAR PRADESH	04/2011	927.01 -	1,400.00	1,331.76	03/2019 -	06/2022	39	51.02	
301	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL, ODISHA	03/2009	942.95 -	1,536.00	1,089.84	03/2019 -	06/2022	39	62.89	
302	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL, UTTAR PRADESH	03/2012	1,183.25 -	1,825.00	1,411.49	12/2020 -	12/2022	24	54.24	
303	VARANASI-MODHOSINGH- ALLAHABAD DOUBLING - [N22000401]RVNL, UTTAR PRADESH	04/2015	943.60 -	1,000.00	688.03	03/2022 -	12/2024	33	5.98	
304	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL, UTTAR PRADESH	04/2015	1,765.92 -	1,765.92	887.48	03/2023 -	12/2024	21	0	
305	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	4,259.48	2,734.83	03/2016 -	03/2025	108	7.78	
306	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	4,639.00	1,119.31	03/2016 -	03/2025	108	59.22	
307	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL, UTTARAKHAND	04/2011	16,216.00 -	22,716.11	2,997.71	12/2024 -	03/2025	3	40.08	
308	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,733.86	40.46	03/2014 -	12/2025	141	18.95	
309	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL, ODISHA	01/1991	2,335.67 -	3,327.72	1,317.36	12/2024 -	12/2026	24	42.47	
	<u>South Central Railway</u>									
310	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR, MULTI STATE	04/2010	704.31 -	927.94	534.34	03/2020 03/2022	06/2021	15	31.75	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
311	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA	04/2017	119.73 185.00	449.39	7.09	03/2022 -	12/2022	9	275.34	
312	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 1.00	3,421.35	1,895.77	03/2000 -	03/2023	276	98.57	
313	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 -	2,120.16	883.52	03/2009 -	03/2024	180	102.85	
314	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	1,160.48 -	1,160.48	502.93	03/2010 -	03/2024	168	0	
315	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 -	1,952.68	567.51	03/2023 -	03/2024	12	5.16	
316	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	2,288.70 -	2,643.25	1,231.85	03/2021 -	03/2024	36	15.49	
317	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	2,063.03	1,416.78	03/2021 -	03/2024	36	0	
318	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	3,887.48	1,144.64	03/2022 -	03/2024	24	7.06	
319	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,132.77 -	3,037.95	350.54	03/2014 -	03/2027	156	42.44	
	<u>South East Central Railway</u>									
320	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	511.86 -	2,005.25	1,777.22	04/2020 -	04/2021	12	291.76	
321	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH	04/2010	585.93 -	1,268.32	941.56	02/2019 -	12/2021	34	116.46	
322	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA	09/2016	1,908.51 -	3,524.81	982.38	03/2023 -	12/2023	9	84.69	
323	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATISGARH	04/2015	1,973.00 -	2,135.34	351.35	03/2021 -	12/2023	33	8.23	
324	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH	04/2015	1,370.00 -	1,370.94	470.49	12/2021 -	12/2023	24	.07	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
325	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA	06/2018	229.00 -	1,096.00	39.79	12/2021 -	12/2024	36	378.6	
	<u>South Eastern Railway</u>									
326	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 358.68	358.68	314.33	12/2018 12/2018	04/2021	28	38.92	
327	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 1,312.96	1,312.96	940.00	03/2020 03/2020	12/2021	21	35.38	
328	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	1,724.20	839.51	03/2021 03/2021	12/2023	33	0	
329	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	651.00 -	1,009.00	7.96	03/2015 -	03/2025	120	54.99	
330	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 1,966.70	2,373.00	485.04	03/2003 -	03/2030	324	130.97	
	<u>South Western Railway</u>									
331	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	1,147.00	911.86	03/2020 -	06/2021	15	33.31	
332	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA	03/2015	578.00 -	783.00	620.29	03/2020 06/2021	06/2021	15	35.47	
333	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,156.94 -	1,656.00	1,160.49	03/2020 03/2023	03/2023	36	43.14	
334	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	986.30 -	986.30	312.23	03/2016 -	12/2023	93	0	
335	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 -	279.54	35.29	03/2016 -	12/2023	93	0	
336	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 -	1,382.78	7.35	03/2002 -	03/2024	264	0	
337	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	832.47	.94	03/2016 -	03/2024	96	0	
338	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 -	1,870.41	1,341.15	03/2019 03/2024	03/2024	60	15.84	
339	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 -	998.00	463.45	03/2017 03/2025	03/2025	96	54.78	
340	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 -	2,841.84	304.83	12/2018 -	06/2025	78	0	
	<u>Southern Railway</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
341	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	950.00	928.36	03/2005 -	09/2021	198	253.33	
342	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU	02/2015	1,700.00 -	1,305.00	756.45	03/2022 -	06/2022	3	-23.24	
343	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU	02/2015	760.00 -	1,536.00	1,233.08	03/2020 -	06/2022	27	102.11	
344	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	1,720.00	701.37	03/2020 -	03/2025	60	465.83	
345	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' - AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	2,910.84	1,621.40	02/2019 -	03/2025	73	301.67	
346	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	1,567.00	-	03/2024 -	03/2026	24	0	
347	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	2,172.16	262.36	03/2019 -	12/2027	105	1699.64	
	<u>West Central Railway</u>									
348	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	424.60 -	2,909.99	1,229.79	03/2021 03/2029	03/2023	24	585.35	
349	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH	06/2016	2,478.23 -	2,478.23	477.93	03/2022 -	03/2023	12	0	
350	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH	08/2016	582.13 1,247.64	1,247.64	296.69	03/2022 -	03/2023	12	114.32	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
351	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH	12/2015	1,763.93	1,762.94	1,156.42	03/2020	03/2024	48	-06	Work is suffering badly on this Critical project due pending forest land clearance. The detail position is as under: ¿ Niwas Road to Deoragram: Forest land 46.067 Ha from Railway Km 1261 to 1301 under DFO Singrauli in isolated patches. Application has been uploaded on Sep'2018. As per letter of Principal Secretary MP State Forest deptt dated 4.6.20, approval under Forest act 1980 is not required for Railway land possessed before 1980. As per discussion with APCCF/ Bhopal, proposals for permission of 2055 Nos. trees cutting have been submitted on 18.06.2020 and 21.07.2020. However, APCCF/Bhopal vide letter dated 31.07.2020 has sought clarifications from MOEF. MOEF vide letter dated 24.09.2020 has clarified that case need to be processed further in FCA. GM/WCR vide letter dated 09.10.2020 has requested Railway Board to intervene in this matter. A meeting was held in Collector Singrauli office on 12.12.20. This meeting was chaired by Hon'ble MP/ Sidhi Smt Riti Pathak. Collector Singrauli has been requested to expedite this proposal. ¿ Vijaysota to Beohari: Forest Land 66.69 Ha under DFO Shahdol from Rly Km 1162 to 1189 in isolated patches. Application has been uploaded in Feb'2019. As per letter of Principal Secretary MP State Forest deptt dated 4.6.20, approval under Forest act 1980 is not required for Railway land possessed before 1980. As per discussion with APCCF/ Bhopal, proposals for permission of 17454 Nos trees cutting have been submitted on 18.08.2020

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
352	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [N220100232]WCR,MULTI STATE	09/1998	247.66 -	8,248.50	2,131.17	05/2008 -	03/2025	202	3230.57	
	<u>Western Railway</u>									
353	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT	02/1991	551.51 890.76	890.76	745.11	03/2019 10/2021	10/2021	31	61.51	
354	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	1,037.15 1,389.05	1,389.05	1,125.73	03/2021 12/2021	12/2021	9	33.93	
355	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 1,002.39	1,002.39	653.86	03/2021 12/2022	12/2022	21	0	
356	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 411.62	411.62	126.05	03/2012 03/2023	03/2023	132	29.34	
357	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 1,347.26	1,347.26	907.54	03/2022 03/2023	03/2023	12	0	
358	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 1,640.04	1,640.04	866.42	03/2022 03/2023	03/2023	12	0	
359	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 1,378.11	1,378.11	540.09	03/2019 03/2023	03/2023	48	329.77	
360	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH	04/2016	700.00 603.69	603.69	254.73	06/2020 03/2023	03/2023	33	-13.76	
361	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	3,503.69 5,912.40	5,912.40	2,161.74	03/2022 03/2024	03/2024	24	68.75	
362	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	829.74 1,959.74	1,959.74	1,799.00	03/2020 03/2024	03/2024	48	136.19	
	Total		1,93,860.66 -	3,18,478.11	1,57,559.01					
	<u>ROAD TRANSPORT AND HIGHWAYS</u>									
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
363	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]MoRTH,MADHYA PRADESH	11/2013	497.05 -	881.05	754.27	05/2017 -	04/2021	47	77.26	
364	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]MoRTH,ANDHRA PRADESH	03/2016	995.09 995.00	995.09	476.77	05/2016 -	04/2021	59	0	
365	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM - [N24000958]MoRTH,RAJASTHAN	02/2018	370.30 -	370.30	290.00	06/2018 -	04/2021	34	0	
366	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]MoRTH,MADHYA PRADESH	12/2015	957.54 -	957.54	756.69	02/2020 04/2021	04/2021	14	0	
367	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]MoRTH,WEST BENGAL	02/2018	218.70 218.70	218.70	104.09	11/2020 04/2020	04/2021	5	0	
368	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH	11/2017	249.05 -	249.05	195.13	07/2018 03/2021	04/2021	33	0	
369	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]MoRTH,MADHYA PRADESH	03/2016	877.79 -	877.79	687.99	06/2019 04/2021	04/2021	22	0	
370	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]MoRTH,ANDHRA PRADESH	02/2017	429.43 -	429.43	256.15	11/2017 04/2021	04/2021	41	0	
371	BARASGAON TO RAHATEE - [N24001113]MoRTH,MAHARASHTRA	07/2016	289.11 290.00	289.11	101.90	09/2018 -	04/2021	31	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
372	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]MoRTH,UTTAR PRADESH	10/2013	445.89 653.00	653.29	754.40	03/2017 -	04/2021	49	46.51	
373	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]MoRTH,UTTAR PRADESH	03/2018	263.89 -	242.05	188.43	04/2020 -	04/2021	12	-8.28	
374	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]MoRTH,WEST BENGAL	01/2017	396.86 396.86	396.86	242.98	09/2019 11/2020	05/2021	20	0	
375	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]MoRTH,MADHYA PRADESH	01/2016	809.16 -	809.16	573.85	07/2018 05/2021	05/2021	34	0	
376	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH,PUNJAB	03/2018	170.57 -	170.57	54.53	11/2020 -	05/2021	6	0	
377	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALAT JUNCTION) TO KM 420.800(P - [N24000963]MoRTH,ANDHRA PRADESH	01/2018	418.03 -	418.03	194.62	08/2018 05/2021	05/2021	33	0	
378	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969]MoRTH,ANDHRA PRADESH	01/2017	263.45 -	263.45	97.45	09/2017 -	05/2021	44	0	
379	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA	02/2017	157.32 188.00	157.32	-	05/2019 -	05/2021	24	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
380	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]MoRTH,UTTAR PRADESH	03/2016	296.50 -	296.50	199.95	09/2020 -	05/2021	8	0	
381	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]MoRTH,MIZORAM	08/2010	193.69 -	327.92	301.46	10/2010 -	06/2021	128	69.3	
382	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]MoRTH,SIKKIM	04/2013	151.59 370.01	370.01	281.74	08/2013 06/2021	06/2021	94	144.09	
383	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]MoRTH,SIKKIM	04/2013	166.27 359.92	359.92	243.59	08/2013 06/2021	06/2021	94	116.47	
384	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]MoRTH,SIKKIM	01/2013	182.28 369.64	369.64	274.07	02/2013 06/2021	06/2021	100	102.79	
385	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]MoRTH,MIZORAM	08/2010	195.04 -	377.99	331.49	10/2010 -	06/2021	128	93.8	
386	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH	11/2015	628.45 -	628.45	439.63	01/2020 01/2021	06/2021	17	0	
387	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH,MADHYA PRADESH	03/2015	511.83 -	511.83	375.50	08/2017 06/2021	06/2021	46	0	
388	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH	03/2018	162.56 -	162.56	129.98	03/2018 -	06/2021	39	0	
389	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH,MADHYA PRADESH	02/2018	169.63 -	169.63	46.52	03/2018 -	06/2021	39	0	
390	UPGRADATION OF PACHORE-SHUJALPUR ROAD TO 2L + PS - [N24000881]MoRTH,MADHYA PRADESH	11/2017	184.62 -	184.62	86.32	02/2018 06/2021	06/2021	40	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
391	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH	01/2017	205.05 -	205.05	123.20	03/2017 -	06/2021	51	0	
392	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH	03/2018	233.04 -	233.04	158.22	03/2018 -	06/2021	39	0	
393	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]MoRTH,MADHYA PRADESH	11/2017	254.17 -	254.17	164.68	02/2018 03/2021	06/2021	40	0	
394	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH	02/2018	279.44 -	279.44	156.14	03/2018 12/2020	06/2021	39	0	
395	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]MoRTH,MADHYA PRADESH	01/2017	373.82 -	373.82	197.04	09/2019 06/2021	06/2021	21	0	
396	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929]MoRTH,ANDHRA PRADESH	09/2016	372.68 -	372.68	185.04	02/2017 06/2021	06/2021	52	0	
397	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000959]MoRTH,RAJASTHAN	02/2018	341.79 -	341.79	208.00	05/2018 -	06/2021	37	0	
398	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]MoRTH,MAHARASHTRA	03/2016	536.65 356.00	536.65	539.35	12/2019 06/2021	06/2021	18	0	
399	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MoRTH,MADHYA PRADESH	11/2017	392.33 428.55	428.55	351.92	03/2018 06/2021	06/2021	39	9.23	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
400	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]MoRTH,MIZORAM	08/2010	186.96 -	322.24	298.52	09/2014 -	06/2021	81	72.36	
401	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]MoRTH,CHHATISGARH	01/2016	497.14 572.66	572.66	270.56	08/2016 06/2021	06/2021	58	15.19	
402	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218]MoRTH,CHHATISGARH	11/2015	335.32 -	335.32	269.15	06/2017 06/2021	06/2021	48	0	
403	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]MoRTH,CHHATISGARH	01/2016	476.20 543.73	544.00	400.38	09/2016 06/2021	06/2021	57	14.24	
404	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]MoRTH,CHHATISGARH	01/2016	624.98 731.50	731.50	416.16	10/2016 06/2021	06/2021	56	17.04	
405	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222]MoRTH,CHHATISGARH	03/2016	452.94 435.61	435.61	94.34	07/2016 06/2021	06/2021	59	-3.83	
406	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226]MoRTH,CHHATISGARH	12/2014	496.02 -	496.02	240.11	03/2015 06/2021	06/2021	75	0	
407	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228]MoRTH,CHHATISGARH	11/2017	188.80 -	188.80	78.69	05/2019 06/2021	06/2021	25	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
408	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 - [N24001229]MoRTH,CHHATISGARH	12/2014	379.16 -	379.16	272.43	11/2017 06/2021	06/2021	43	0	
409	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 KM - [N24001230]MoRTH,UTTAR PRADESH	11/2018	281.45 -	281.45	72.05	12/2020 -	06/2021	6	0	
410	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931]MoRTH,ANDHRA PRADESH	11/2016	290.15 -	290.15	73.11	05/2017 07/2021	07/2021	50	0	
411	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966]MoRTH,ANDHRA PRADESH	01/2016	348.95 -	348.95	200.57	08/2016 -	07/2021	59	0	
412	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]MoRTH,TRIPURA	10/2016	171.90 -	171.90	123.81	08/2020 -	07/2021	11	0	
413	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905]MoRTH,PUNJAB	03/2018	322.48 -	322.48	271.72	07/2020 -	08/2021	13	0	
414	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH,PUNJAB	10/2017	1,069.59 -	1,069.59	692.14	10/2019 -	08/2021	22	0	
415	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH	03/2018	214.69 -	214.69	69.34	03/2018 -	09/2021	42	0	
416	UPGRADATION OF PORSABHIND ROAD TO 2L + PS - [N24000890]MoRTH,MADHYA PRADESH	03/2018	217.22 -	226.88	170.96	08/2018 09/2021	09/2021	37	4.45	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
417	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]MoRTH,MADHYA PRADESH	11/2011	954.43 -	1,191.51	235.61	09/2015 -	10/2021	73	24.84	
418	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]MoRTH,MADHYA PRADESH	01/2019	264.50 -	264.50	85.70	03/2021 11/2021	11/2021	8	0	
419	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]MoRTH,WEST BENGAL	02/2018	426.18 426.18	426.18	249.01	09/2020 -	12/2021	15	0	
420	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH,WEST BENGAL	06/2016	236.78 263.26	263.26	65.84	08/2019 -	12/2021	28	11.18	
421	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGOUR SECTION BY EXECUTING BALANCE WORK FRO - [N24001241]MoRTH,RAJASTHAN	03/2020	255.23 -	255.23	1.66	08/2020 -	08/2022	24	0	
422	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K - [N24001242]MoRTH,RAJASTHAN	08/2020	196.23 -	196.00	-	11/2020 -	08/2022	21	-12	
423	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH,WEST BENGAL	03/2016	160.27 213.97	213.97	25.64	08/2019 -	11/2022	39	33.51	
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>									
424	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM	01/2016	294.17 -	294.17	121.82	01/2016 -	04/2021	63	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
425	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	387.00	245.80	08/2016 -	05/2021	57	3.73	
426	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	339.55	252.49	08/2016 -	05/2021	57	-14.37	
427	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 -	340.00	193.99	08/2016 -	05/2021	57	-20.84	
428	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL,MANIPUR	08/2017	517.57 -	457.77	137.04	10/2018 -	10/2021	36	-11.55	
429	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND	03/2018	215.12 -	215.12	100.90	09/2018 -	11/2021	38	0	
430	4 LANING OF JORHAT TO JHANJHI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM	06/2015	437.39 -	407.30	21.46	06/2018 -	12/2021	42	-6.88	
431	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM	06/2015	463.49 -	398.06	59.71	06/2018 -	12/2021	42	-14.12	
432	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND	03/2018	315.03 -	315.03	88.52	09/2018 -	12/2021	39	0	
433	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND	03/2018	240.64 -	240.64	102.51	09/2018 -	12/2021	39	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
434	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND	03/2018	215.79 -	215.79	67.30	09/2018 -	12/2021	39	0	
435	CONSTRUCTION OF MEKAROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH	01/2017	1,253.10 -	1,253.10	204.77	03/2017 -	03/2022	60	0	
436	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND	03/2018	239.30 -	239.30	102.01	09/2018 -	05/2022	44	0	
437	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND	03/2018	339.57 -	339.57	141.46	09/2018 -	07/2022	46	0	
438	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND	03/2018	285.68 -	285.68	77.91	09/2018 -	09/2022	48	0	
439	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND	03/2018	272.89 -	272.89	51.17	09/2018 -	10/2022	49	0	
440	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND	03/2018	500.09 336.49	336.49	79.51	09/2018 -	11/2022	50	-32.71	
441	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND	03/2018	323.98 -	323.98	42.54	09/2018 -	11/2022	50	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
442	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM	04/2017	519.09 -	519.09	56.58	09/2019 -	04/2023	43	0	
443	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM	04/2017	473.18 -	473.18	81.00	09/2019 -	04/2023	43	0	
444	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM	04/2017	537.82 -	537.82	100.74	09/2019 -	04/2023	43	0	
445	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM	04/2017	642.96 -	642.96	82.00	09/2019 -	06/2023	45	0	
446	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM	04/2017	518.53 -	518.53	108.99	09/2019 -	06/2023	45	0	
447	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM	04/2017	640.07 -	640.07	3.25	09/2019 -	07/2023	46	0	
448	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM	04/2017	428.11 -	428.11	48.03	09/2019 -	09/2023	48	0	
449	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM	04/2017	404.29 -	404.29	17.77	09/2019 -	04/2024	55	0	
	<u>National Highways Authority Of India</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
450	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH	03/2018	1,532.62 -	2,499.00	761.73	03/2021 10/2021	04/2021	1	63.05	
451	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,295.18	08/2013 -	05/2021	93	0	
452	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA	03/2017	639.79 -	552.90	597.77	03/2020 05/2021	05/2021	14	-13.58	
453	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	227.77	36.08	03/2020 -	05/2021	14	-3.27	
454	4-LANNING OF THALSERRY - MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	1,232.76	527.67	09/2017 -	05/2021	44	9.67	
455	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	3,182.34	3,087.00	04/2015 01/2021	06/2021	74	65.04	
456	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	730.97	653.06	05/2018 06/2021	06/2021	37	37.63	
457	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	690.17	595.33	05/2018 06/2021	06/2021	37	16.34	
458	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	504.00	385.08	05/2018 04/2019	06/2021	37	-2	
459	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	1,420.00	842.24	03/2020 -	06/2021	15	10.24	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
460	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI, ODISHA	07/2017	476.56 -	476.56	52.19	07/2017 -	06/2021	47	0	
461	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI, RAJASTHAN	04/2017	894.00 -	929.32	810.00	04/2020 -	07/2021	15	3.95	
462	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI, TAMIL NADU	05/2010	374.00 -	166.90	54.22	05/2013 -	08/2021	99	-55.37	
463	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI, HARYANA	07/2015	2,128.72 -	2,128.72	1,070.00	04/2019 -	09/2021	29	0	
464	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI, HIMACHAL PRADESH	06/2017	2,485.93 -	2,485.93	827.64	06/2020 -	09/2021	15	0	
465	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI, MAHARASHTRA	03/2016	546.00 -	546.00	307.08	07/2019 06/2021	12/2021	29	0	
466	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI, MAHARASHTRA	03/2016	591.66 -	591.66	318.30	07/2019 06/2021	12/2021	29	0	
467	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI, KARNATAKA	08/2016	1,167.42 -	870.00	333.68	03/2019 01/2021	12/2021	33	-25.48	
468	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250 (DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI, TAMIL NADU	03/2017	848.45 932.23	848.45	222.06	03/2020 -	12/2021	21	0	
469	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI, PUNJAB	03/2017	754.54 -	756.27	379.05	03/2020 -	12/2021	21	.23	
470	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE - [N24001231]NHAI, MADHYA PRADESH	02/2019	990.97 -	990.97	569.29	12/2019 -	12/2021	24	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
471	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	624.00	8.56	04/2014 -	01/2022	93	0	
472	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	950.64	200.18	08/2017 -	02/2022	54	0	
473	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	649.50	209.18	03/2019 12/2021	03/2022	36	0	
474	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	701.40	132.05	03/2019 03/2022	03/2022	36	0	
475	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO - [N24001232]NHAI,MADHYA PRADESH	02/2019	847.00 -	847.00	393.93	03/2020 -	04/2022	25	0	
476	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS- CONTROLLED EXPRESSWAY FROM BAWDI VILLAGE - [N24001233]NHAI,MADHYA PRADESH	03/2019	1,047.00 -	1,047.00	367.12	05/2020 -	05/2022	24	0	
477	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,878.70	08/2013 -	06/2022	106	0	
478	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	1,176.37	462.14	08/2017 -	07/2022	59	0	
479	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	1,227.87	566.14	09/2017 -	07/2022	58	0	
480	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	3,379.45	2,901.20	03/2014 -	12/2022	105	18.66	
	Total		65,750.54 -	70,242.14	39,633.71					
	TELECOMMUNICATIONS									
	Bharat Sanchar Nigam Limited									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
481	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114]BSNL,MULTI STATE	03/2020	431.16 431.00	431.16	-	06/2021 -	11/2021	5	0	
	<u>Central Public Works Department</u>									
482	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI	10/2016	248.20 -	248.20	145.26	03/2018 -	06/2021	39	0	
	<u>Department Of Telecommunication</u>									
483	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	24,664.00	17,845.00	07/2015 -	07/2021	72	84.97	
	Total		14,013.36 -	25,343.36	17,990.26					
	<u>URBAN DEVELOPMENT</u>									
	<u>Ahmedabad Metro Rail</u>									
484	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT	11/2014	10,773.00 -	12,787.00	8,768.08	12/2018 -	08/2022	44	18.69	
	<u>Bangalore Metro Rail Corporation Limited</u>									
485	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA	02/2014	26,405.14 30,695.12	30,695.12	17,021.86	02/2019 03/2021	06/2024	64	16.25	
	<u>Central Public Works Department</u>									
486	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00 -	422.00	70.75	03/2021 07/2021	07/2021	4	0	
487	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI	06/2015	197.33 -	197.33	106.16	04/2019 06/2021	12/2021	32	0	
488	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 -	392.00	73.79	08/2020 -	03/2022	19	0	
489	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I - [N28000128]CPWD,DELHI	10/2016	1,180.00 -	1,100.80	35.63	07/2021 -	12/2024	41	-6.71	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>Delhi Metro Rail Corporation</u>									
490	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	38,585.00	39,182.53	03/2016 -	09/2021	66	0	
491	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136]DMRC,DELHI	05/2017	565.00 -	565.00	438.37	12/2020 -	09/2021	9	0	
	<u>Mumbai Metro Rail Corporation Ltd</u>									
492	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	33,406.00	17,039.36	01/2015 -	03/2023	98	44.39	
	Total		1,01,655.47 -	1,18,150.25	82,736.53					
	<u>WATER RESOURCES</u>									
	<u>Brahmaputra Board</u>									
493	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPB,MAHARASHTRA	03/2017	233.57 -	233.57	173.71	12/2019 -	12/2021	24	0	
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>									
494	I AND D AND STP AT CHAPPRA - [N30000028]BUIDCO,BIHAR	11/2018	236.15 -	236.15	46.50	12/2020 06/2021	04/2021	4	0	
495	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR - [N30000038]BUIDCO,BIHAR	04/2015	184.93 -	184.93	163.36	04/2020 -	06/2021	14	0	
496	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]BUIDCO,BIHAR	03/2018	305.19 -	305.19	-	08/2021 -	12/2021	4	0	
	<u>Delhi Jal Board</u>									
497	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI - [N30000017]DJB,DELHI	12/2018	515.07 -	515.07	336.27	01/2021 -	06/2021	5	0	
498	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015]DJB,DELHI	05/2016	211.79 -	211.79	87.31	12/2021 -	12/2022	12	0	
499	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]DJB,DELHI	05/2016	239.11 -	239.11	129.67	02/2022 -	12/2022	10	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>Kolkata Metropolitan Development Authority</u>									
500	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046]KMDA, WEST BENGAL	02/2014	274.76 -	274.76	202.13	12/2019 05/2021	05/2021	17	0	
501	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]KMDA, WEST BENGAL	05/2018	198.43 224.69	224.69	-	02/2022 -	06/2022	4	13.23	
502	INTERCEPTION AND DIVERSION WITH STP AT HUGLY-CHINSURAH - [N30000042]KMDA, WEST BENGAL	05/2018	160.00 154.73	154.73	-	02/2022 -	10/2022	8	-3.29	
	<u>Polavaram Project Authority</u>									
503	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA, ANDHRA PRADESH	02/2009	10,151.04 55,548.87	55,548.87	17,325.20	03/2020 11/2021	04/2022	25	447.22	
	<u>Uttar Pradesh Jal Nigam</u>									
504	MATHURA SEWERAGE SCHEME - [N30000019]UP JalNigam, UTTAR PRADESH	12/2017	460.45 -	460.45	216.89	12/2020 -	05/2021	5	0	
505	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]UP JalNigam, UTTAR PRADESH	03/2019	298.12 213.91	213.91	-	07/2021 -	06/2022	11	-28.25	
	Total		13,468.61 -	58,803.22	18,681.04					
	<u>DEFENCE PRODUCTION</u>									
	<u>Central Public Works Department</u>									
506	RESIDENTIAL QUARTERS FOR HAL, BANGLORE - [N28000103]CPWD, KARNATAKA	12/2016	246.31 -	210.00	131.46	02/2020 -	12/2021	22	-14.74	
	Total		246.31 -	210.00	131.46					
	<u>HUMAN RESOURCE DEVELOPMENT</u>									
507	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]CPWD, PUNJAB	08/2016	294.00 -	350.69	276.69	04/2019 -	05/2021	25	19.28	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
508	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	111.29	03/2016 -	06/2021	63	0	
509	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH	11/2017	171.72 -	171.72	53.94	03/2020 -	06/2021	15	0	
510	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]CPWD,MAHARASHTRA	01/2018	223.37 -	223.37	61.35	07/2020 -	06/2021	11	0	
511	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	498.99	224.58	06/2017 -	10/2021	52	.57	
512	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB - [N28000120]CPWD,PUNJAB	01/2018	430.00 -	387.83	199.99	05/2020 -	02/2022	21	-9.81	
513	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD,ODISHA	01/2019	790.79 -	790.79	173.98	03/2022 -	06/2022	3	0	
514	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE,KANJIKODE WEST, DISTRICT PALAKKA - [N28000140]CPWD,KERALA	07/2019	753.63 -	753.63	58.47	03/2021 -	06/2022	15	0	
515	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB. - [N28000142]CPWD,PUNJAB	10/2019	348.24 -	348.24	18.71	05/2022 -	08/2022	3	0	
516	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A) - [N42000006]CPWD,KARNATAKA	07/2019	851.00 851.00	851.00	26.10	03/2022 -	09/2022	6	0	
517	PERMANENT CAMPUS FOR IIM BODH GAYA - [N42000009]CPWD,BIHAR	09/2018	375.00 -	375.00	48.46	09/2020 -	11/2022	26	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
518	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRICT - [N42000007]CPWD,ANDHRA PRADESH	09/2019	588.72 -	588.72	14.80	09/2022 -	01/2023	4	0	
	Total		5,494.51 -	5,511.84	1,268.36					
	<u>HOME AFFAIRS</u>									
519	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	2,000.00	906.04	10/2019 -	12/2021	26	64.04	
520	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL	10/2014	162.88 238.00	238.00	171.19	04/2018 12/2021	12/2021	44	46.12	
	Total		1,382.09 -	2,238.00	1,077.23					
	<u>RURAL DEVELOPMENT</u>									
	<u>Hindustan Steelwork Construction Limited</u>									
521	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	155.66	144.95	12/2015 -	10/2021	70	3.96	
522	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	207.12	190.22	12/2016 -	10/2021	58	2.23	
523	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	175.49	124.87	12/2016 -	12/2021	60	0	
	Total		527.83 -	538.27	460.04					
	<u>DPIIT</u>									
	<u>Delhi Mumbai Industrial Corridor</u>									
524	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]DMIC,MULTI STATE	09/2011	12,579.09 -	13,812.30	8,915.05	09/2019 01/2014	07/2021	22	9.8	
	<u>India International Convention And Expo Centre</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
525	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]IICC, DELHI	11/2017	4,773.00 -	5,178.00	2,557.37	12/2019 -	12/2021	24	8.49	
	Total		17,352.09 -	18,990.30	11,472.42					
	Grand Total		9,15,431.94	11,97,201.16	6,87,640.77					

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Annexure - VII

(April 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	<u>ATOMIC ENERGY</u>								
	<u>Bhavini Limited</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,840.00	5,935.96	09/2010 -	10/2022	95.88	145
	<u>Nuclear Power Corporation Of India Limited</u>								
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	16,488.00	12/2015 -	02/2022	44.69	74
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) [N02000027]	10/2009	12,320.00 -	17,079.00	13,206.00	12/2016 -	03/2023	38.63	75
	Total		27,271.00 -	40,499.00	35,629.96				
	<u>CIVIL AVIATION</u>								
	<u>Airport Authority Of India Limited</u>								
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	417.23 -	707.73	379.95	09/2018 -	06/2021	69.63	33
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]	12/2016	1,142.00 -	1,232.00	368.37	03/2021 -	03/2022	7.88	12
	Total		1,559.23 -	1,939.73	748.32				
	<u>COAL</u>								
	<u>Bharat Coking Coal Limited</u>								
6	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]	10/2015	243.00 -	334.27	18.35	04/2018 -	06/2022	37.56	50
7	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]	12/2015	304.13 -	341.22	40.84	03/2017 -	03/2022	12.20	60
	<u>Neyveli Lignite Corporation</u>								
8	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW [N06000152]	07/2016	17,237.00 -	17,237.80	11,574.21	11/2021 -	07/2022	.00	8
	<u>Singareni Colliers Company Limited</u>								
9	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	251.14	03/2015 -	03/2022	114.60	84
10	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	109.25	03/2019 -	03/2022	11.42	36
11	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 -	473.22	79.04	03/2015 -	03/2023	5.85	96

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(April 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
12	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	416.07	03/2012 -	03/2023	16.86	132
	<u>South-Eastern Coal Fields Limited</u>								
13	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	202.90	03/2015 -	03/2022	201.44	84
	<u>Western Coal Fields Limited</u>								
14	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]	09/2016	289.29 -	289.30	35.95	03/2022 -	03/2025	.00	36
15	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]	02/2016	198.68 -	325.18	253.17	03/2019 -	03/2022	63.67	36
16	ADASA UG TO OC - [N06000133]	08/2015	288.90 -	333.43	142.27	03/2023 -	03/2024	15.41	12
17	KOLAR PIMPRI EXTENSION OC - [N06000160]	03/2017	362.73 -	402.90	330.34	03/2020 -	09/2022	11.07	30
18	NEW MAJRI UG TO OC - [N06000128]	05/2015	295.56 -	496.38	164.25	03/2019 -	09/2026	67.95	90
19	BHATADI EXPANSION OC MINE - [N06000150]	02/2016	304.52 -	729.86	160.67	03/2019 -	09/2026	139.68	90
	Total		21,102.12 -	22,704.37	13,778.45				
	<u>DPIIT</u>								
	<u>Delhi Mumbai Industrial Corridor</u>								
20	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]	09/2011	12,579.09 -	13,812.30	8,915.05	09/2019 -	07/2021	9.80	22
	<u>India International Convention And Expo Centre</u>								
21	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]	11/2017	4,773.00 -	5,178.00	2,557.37	12/2019 -	12/2021	8.49	24
	Total		17,352.09 -	18,990.30	11,472.42				
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Hospital Services Consultancy Corporation Ltd</u>								
22	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	02/2013	414.11 -	499.23	494.72	11/2013 -	05/2021	20.55	90
	Total		414.11 -	499.23	494.72				
	<u>HOME AFFAIRS</u>								
	<u>Central Public Works Department</u>								
23	NSG AT KOLKATA - [N28000104]	10/2014	162.88 -	238.00	171.19	04/2018 -	12/2021	46.12	44

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(April 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
24	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	2,000.00	906.04	10/2019 -	12/2021	64.04	26
	Total		1,382.09 -	2,238.00	1,077.23				
	<u>HUMAN RESOURCE DEVELOPMENT</u>								
25	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]	08/2016	294.00 -	350.69	276.69	04/2019 -	05/2021	19.28	25
26	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	224.58	06/2017 -	10/2021	.57	52
	Total		790.18 -	849.68	501.27				
	<u>PETROLEUM</u>								
	<u>Bharat Petroleum Corporation Limited</u>								
27	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]	11/2012	678.00 -	1,472.00	19.44	02/2017 -	08/2022	117.11	66
28	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]	12/2015	1,112.00 -	1,507.24	730.00	06/2019 -	02/2022	35.54	32
29	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29 -	5,245.96	5,076.00	08/2018 -	05/2021	14.33	33
	<u>Gas Authority Of India Limited</u>								
30	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECT - [N16000349]	09/2018	225.54 -	247.90	40.10	02/2021 -	12/2021	9.91	10
31	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]	08/2018	286.42 -	327.01	186.00	08/2020 -	06/2021	14.17	10
32	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]	06/2009	2,915.00 2,915.00	5,909.00	3,607.20	12/2012 -	02/2022	102.71	110
	<u>Hindustan Petroleum Corporation Limited</u>								
33	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]	11/2017	255.00 -	300.00	271.70	11/2020 -	06/2021	17.65	7
34	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	09/2017	2,677.00 -	3,072.00	2,239.96	06/2021 -	08/2022	14.76	14
35	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	07/2016	20,928.00 -	26,264.00	14,820.38	07/2020 -	07/2022	25.50	24
	<u>Indian Oil Corporation Limited</u>								

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(April 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
36	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304	08/2017	236.00 -	293.00	161.05	06/2020 -	09/2021	24.15	15
37	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR), CACHAR, ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236	06/2016	423.00 -	502.00	422.12	08/2019 -	06/2021	18.68	22
38	LPG TERMINAL AT KOCHI - [N16000171	10/2015	607.06 -	1,236.00	394.74	10/2017 -	03/2022	103.60	53
39	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193	01/2015	1,823.00 -	3,027.90	1,957.55	03/2021 -	12/2021	66.09	9
40	PARADIP HYDERABAD PIPELINE - [N16000194	01/2015	2,321.00 -	3,338.00	2,923.70	12/2020 -	03/2022	43.82	15
41	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253	05/2016	4,497.00 -	6,025.00	3,681.97	12/2018 -	02/2022	33.98	38
	<u>Mangalore Refinery And Petrochemicals Limited</u>								
42	SEA WATER DESALINATION PLANT - [N16000319	11/2017	581.00 -	637.00	489.10	03/2020 -	07/2021	9.64	16
	<u>Oil & Natural Gas Corporation Limited</u>								
43	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278	07/2016	249.85 250.00	303.75	199.31	05/2020 -	05/2021	21.57	12
44	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128	03/2011	861.79 -	2,001.00	1,551.48	05/2013 -	02/2022	132.19	105
45	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213	12/2015	3,190.69 -	3,375.90	2,786.78	04/2018 -	05/2022	5.80	49
46	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359	05/2019	3,660.71 -	3,740.05	2,808.52	05/2021 -	01/2022	2.17	8
47	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358	04/2019	3,228.80 -	3,976.67	1,188.33	03/2022 -	05/2023	23.16	14
	<u>Oil India Limited</u>								
48	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331	01/2018	543.91 -	652.10	320.30	02/2020 -	06/2021	19.89	16
	Total		55,889.06 -	73,453.48	45,875.73				
	<u>POWER</u>								
	<u>National Hydro-Electric Power Corporation</u>								
49	PARBATI HEP (4X200 MW) (NHPC) II - [180100210	09/2002	3,919.59 -	9,897.59	8,945.10	09/2009 -	07/2022	152.52	154
50	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221	09/2003	6,285.33 -	19,992.43	13,732.39	09/2010 -	08/2023	218.08	155
	<u>National Thermal Power Corporation</u>								

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(April 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
51	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014	11/2006	2,978.48 -	5,867.38	4,913.02	03/2013 -	12/2022	96.99	117
52	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190	01/2007	5,353.00 -	10,566.00	8,847.06	07/2012 -	07/2021	97.38	108
53	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212	01/2016	10,598.98 -	10,997.70	8,368.64	11/2020 -	07/2022	3.76	20
54	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176	02/2014	12,532.44 -	13,140.91	11,730.23	12/2018 -	05/2021	4.86	29
55	NORTH KARANPURA STPP (3X660 MW) - [N18000177	02/2014	14,366.58 -	15,389.42	11,722.10	06/2019 -	10/2022	7.12	40
56	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192	01/2013	12,964.60 -	17,304.00	15,787.92	05/2018 -	12/2021	33.47	43
57	BARH STPP(3X660MW) NTPC - [180100242	02/2005	8,692.97 -	21,312.11	18,595.56	10/2011 -	07/2023	145.16	141
	<u>Power Grid Corporation Of India Limited</u>								
58	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262	05/2017	186.17 -	219.66	157.20	07/2019 -	06/2021	17.99	23
59	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164	05/2014	522.29 -	546.36	478.29	11/2016 -	06/2021	4.61	55
60	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258	03/2017	3,500.00 3,500.00	3,994.00	2,917.31	07/2020 -	06/2021	14.11	11
61	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250	12/2014	5,111.33 -	6,700.00	2,767.14	12/2018 -	12/2021	31.08	36
62	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249	12/2014	4,754.42 -	9,129.32	2,163.30	12/2018 -	03/2024	92.02	63
63	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066	02/2009	11,130.19 -	14,719.10	12,894.95	08/2013 -	08/2022	32.24	108
	<u>Thdc India Limited</u>								
64	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042	08/2008	2,491.58 -	3,860.35	2,223.06	06/2013 -	12/2023	54.94	126
	Total		1,05,387.95 -	1,63,636.33	126,243.27				
	<u>RAILWAYS</u>								
	<u>Central Railways</u>								
65	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356	02/2015	1,272.19 -	1,283.49	408.70	03/2022 -	03/2023	.89	12
66	KALYAN-KASARA 3RD LINE - [N22000233	04/2011	792.89 -	1,377.48	335.23	03/2021 -	03/2023	73.73	24
67	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181	02/1997	2,271.50 -	4,517.49	2,648.51	03/2021 -	03/2023	98.88	24

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(April 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	<u>East Central Railways</u>								
68	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	477.88 283.95	751.55	694.88	03/2012 -	07/2021	57.27	112
69	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181	04/2009	548.00 -	819.01	535.44	03/2020 -	03/2023	49.45	36
70	HAJIPUR - BACHAWARA - [N22000334	05/2015	678.54 -	929.86	848.39	03/2019 -	05/2021	37.04	26
71	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR [220100240	04/1997	324.73 -	1,070.00	1,069.58	03/2012 -	11/2022	229.50	128
72	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473	04/2016	731.64 -	1,185.73	217.95	03/2021 -	06/2022	62.06	15
73	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472	04/2016	744.04 -	1,215.54	426.72	03/2021 -	03/2024	63.37	36
	<u>East Coast Railway</u>								
74	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319	03/2012	155.81 -	238.03	221.48	03/2020 -	03/2022	52.77	24
75	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380	04/2015	701.61 -	810.02	171.45	11/2018 -	03/2024	15.45	64
76	KIRANDUL - JAGDALPUR DOUBLING - [N22000318	12/2012	1,160.00 -	1,160.83	950.18	03/2020 -	03/2023	.07	36
77	SAMBALPUR-TALCHER DOUBLING - [N22000315	03/2011	1,111.99 -	1,539.28	1,109.06	02/2019 -	12/2021	38.43	34
78	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	810.78 -	1,928.07	873.81	06/2021 -	03/2025	137.80	45
79	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	2,923.13 -	3,791.66	1,506.95	03/2009 -	03/2026	29.71	204
	<u>Eastern Railways</u>								
80	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	12.02	108
81	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229	04/2010	365.17 -	439.30	411.65	03/2017 -	03/2025	20.30	96
82	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240	04/2010	494.54 -	494.59	32.00	03/2005 -	03/2025	.01	240
83	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216	04/1987	406.99 -	545.70	149.31	03/2006 -	03/2025	34.08	228
84	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243	04/2009	499.96 -	680.68	164.09	02/2012 -	03/2025	36.15	157
85	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225	04/2005	595.51 -	769.40	103.86	03/2017 -	03/2025	29.20	96

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(April 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
86	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224	04/2001	923.52 -	995.10	645.97	03/2016 -	03/2025	7.75	108
87	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	607.09 -	1,425.44	638.05	02/2013 -	03/2024	134.80	133
88	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	1,188.91 -	1,619.48	905.06	03/2019 12/2009	03/2025	36.22	72
89	PIRPAINTI-JASIDIH - [N22000219	04/2013	915.98 -	2,137.81	388.53	03/2022 -	03/2025	133.39	36
	<u>Indian Railway Construction Company Limited</u>								
90	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489	04/2013	3,055.00 -	3,055.15	2,431.72	09/2018 -	03/2022	.00	42
91	GEVRA ROAD PENDRA ROAD - [N22000488	02/2014	2,288.00 -	4,970.11	866.16	03/2022 -	12/2023	117.23	21
	<u>Metropolitan Rapid Transport Projects</u>								
92	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028	04/2006	495.74 -	734.01	510.69	06/2013 -	12/2021	48.06	102
93	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	2,980.41	1,768.25	03/2004 -	03/2022	501.57	216
94	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	75.91	63
	<u>North Central Railway</u>								
95	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	04/2011	2,912.96 -	3,845.60	148.26	03/2022 -	12/2024	32.02	33
	<u>North East Frontier Railway</u>								
96	AGARTALA-AKHAURA NL - [N22000195	04/2012	569.63 -	742.00	200.28	03/2020 -	03/2022	30.26	24
97	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086	09/2006	385.20 -	1,043.00	837.67	03/2019 -	03/2023	170.77	48
98	DIGARU-HOJAI (102 KM) - [N22000389	04/2015	870.96 -	1,873.21	1,309.41	03/2021 -	05/2021	115.07	2
99	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183	04/2013	1,798.00 -	2,042.51	136.41	03/2019 -	03/2024	13.60	60
100	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087	09/2006	532.87 -	2,145.00	1,001.65	03/2019 -	03/2024	302.54	60
101	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388	04/2015	2,232.32 -	2,950.00	1,620.12	03/2022 -	03/2023	32.15	12
102	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	1,180.19 -	4,541.38	3,804.55	12/2008 -	05/2021	284.80	149
103	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	2,393.47 -	5,521.45	3,954.28	03/2014 -	03/2023	130.69	108

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(April 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
104	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	2,326.52	6,911.00	1,204.64	03/2015	12/2024	197.05	117
105	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17	12,264.15	10,994.55	03/2011	12/2023	175.34	153
	<u>North Eastern Railway</u>								
106	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00	213.35	12.86	04/2016	12/2021	.16	68
107	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00	477.31	378.98	01/2019	02/2022	61.80	37
	<u>North Western Railway</u>								
108	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTURGARH-UDAIPUR [N22000152]	04/2013	420.18	480.00	357.41	03/2020	06/2021	14.24	15
109	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00	701.81	236.13	03/2020	10/2022	16.97	31
110	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08	860.41	709.62	02/2019	06/2022	109.82	40
	<u>Northern Railway</u>								
111	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00	859.00	852.73	03/2016	06/2021	37.44	63
112	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00	893.45	705.53	12/2011	06/2021	211.31	114
113	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14	1,540.13	242.04	03/2023	03/2025	369.35	24
114	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00	2,200.00	714.78	07/2012	03/2024	388.89	140
115	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00	27,949.00	24,040.61	11/2002	12/2022	1,017.96	241
	<u>Rail Vikas Nigam Ltd.</u>								
116	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD [N22000213]	04/2012	632.68	950.00	810.96	03/2016	12/2021	50.15	69
117	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	943.60	1,000.00	688.03	03/2022	12/2024	5.98	33
118	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01	1,400.00	1,331.76	03/2019	06/2022	51.02	39
119	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95	1,536.00	1,089.84	03/2019	06/2022	62.89	39
120	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION [N22000413]	03/2012	1,183.25	1,825.00	1,411.49	12/2020	12/2022	54.24	24
121	BINA - KOTA DOUBLING WITH RE - [N22000414]	04/2011	1,485.85	1,835.83	1,571.35	12/2020	12/2021	23.55	12
122	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	04/2013	1,548.66	1,868.89	1,831.45	12/2021	03/2022	20.68	3

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(April 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
123	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 -	2,009.00	1,875.48	03/2020 -	12/2021	111.91	21
124	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	1,202.70 -	2,440.53	1,337.54	02/2015 -	06/2022	102.92	88
125	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 -	2,725.00	2,554.71	03/2020 -	12/2021	281.93	21
126	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	40.46	03/2014 -	12/2025	18.95	141
127	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 -	3,327.72	1,317.36	12/2024 -	12/2026	42.47	24
128	VIJAYWADA-GUDUGOLANU-BHIMAVARAM- NARSAPUR DL (221 KM) - [N22000313]	03/2012	1,503.71 -	3,377.00	2,683.67	03/2020 -	03/2022	124.58	24
129	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	2,734.83	03/2016 -	03/2025	7.78	108
130	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	04/2010	2,913.51 -	4,639.00	1,119.31	03/2016 -	03/2025	59.22	108
131	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	04/2011	16,216.00 -	22,716.11	2,997.71	12/2024 -	03/2025	40.08	3
	<u>South Central Railway</u>								
132	MANMAD-PARBHANI-NANDED-SECUNDERABAD- GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	04/2017	119.73 185.00	449.39	7.09	03/2022 -	12/2022	275.34	9
133	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	704.31 -	927.94	534.34	03/2020 -	06/2021	31.75	15
134	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	04/2012	1,856.95 -	1,952.68	567.51	03/2023 -	03/2024	5.16	12
135	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 -	2,120.16	883.52	03/2009 -	03/2024	102.85	180
136	NADIKUDE-SRI KALAHASTI - [N22000286]	04/2011	2,288.70 -	2,643.25	1,231.85	03/2021 -	03/2024	15.49	36
137	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]	04/2008	2,132.77 -	3,037.95	350.54	03/2014 -	03/2027	42.44	156
138	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	1,723.00 1.00	3,421.35	1,895.77	03/2000 -	03/2023	98.57	276
139	GUNTUR-GUNTAKAL - [N22000368]	04/2016	3,631.00 -	3,887.48	1,144.64	03/2022 -	03/2024	7.06	24
	<u>South East Central Railway</u>								
140	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00 -	1,096.00	39.79	12/2021 -	12/2024	378.60	36
141	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438]	04/2010	585.93 -	1,268.32	941.56	02/2019 -	12/2021	116.46	34

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(April 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
142	ANUPPUR-KATNI - [N22000485]	04/2015	1,370.00 -	1,370.94	470.49	12/2021 -	12/2023	.07	24
143	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	511.86 -	2,005.25	1,777.22	04/2020 -	-	291.76	12
144	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	04/2015	1,973.00 -	2,135.34	351.35	03/2021 -	12/2023	8.23	33
145	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,908.51 -	3,524.81	982.38	03/2023 -	12/2023	84.69	9
	<u>South Eastern Railway</u>								
146	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	358.68	314.33	12/2018 -	04/2021	38.92	28
147	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	651.00 -	1,009.00	7.96	03/2015 -	03/2025	54.99	120
148	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	1,312.96	940.00	03/2020 -	12/2021	35.38	21
149	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 -	2,373.00	485.04	03/2003 -	03/2030	130.97	324
	<u>South Western Railway</u>								
150	ARSIKERE-TUMKUR - [N22000332]	03/2015	578.00 -	783.00	620.29	03/2020 -	06/2021	35.47	15
151	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78 -	998.00	463.45	03/2017 -	03/2025	54.78	96
152	YELAHANKA-PENUKONDA - [N22000328]	05/2015	860.43 -	1,147.00	911.86	03/2020 -	06/2021	33.31	15
153	HUBLI- CHIKJAJUR - [N22000325]	03/2015	1,156.94 -	1,656.00	1,160.49	03/2020 -	03/2023	43.14	36
154	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 -	1,870.41	1,341.15	03/2019 -	03/2024	15.84	60
	<u>Southern Railway</u>								
155	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	02/1996	268.87 -	950.00	928.36	03/2005 -	09/2021	253.33	198
156	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00 -	1,536.00	1,233.08	03/2020 -	06/2022	102.11	27
157	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	303.98 -	1,720.00	701.37	03/2020 -	03/2025	465.83	60
158	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70 -	2,172.16	262.36	03/2019 -	12/2027	1,699.64	105
159	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]	09/2007	724.69 -	2,910.84	1,621.40	02/2019 -	03/2025	301.67	73
	<u>West Central Railway</u>								
160	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13 -	1,247.64	296.69	03/2022 -	03/2023	114.32	12

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(April 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
161	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314	04/2001	424.60 -	2,909.99	1,229.79	03/2021 -	03/2023	585.35	24
162	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	247.66 -	8,248.50	2,131.17	05/2008 -	03/2025	3,230.57	202
	<u>Western Railway</u>								
163	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) [N22000123	04/2008	318.24 -	411.62	126.05	03/2012 -	03/2023	29.34	132
164	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487	02/1991	551.51 -	890.76	745.11	03/2019 -	10/2021	61.51	31
165	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143	04/1994	320.66 -	1,378.11	540.09	03/2019 -	03/2023	329.77	48
166	VIRAMGAM-SAMAKHALI (DL) - [N22000145	04/2011	1,037.15 -	1,389.05	1,125.73	03/2021 -	12/2021	33.93	9
167	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121	04/2008	829.74 -	1,959.74	1,799.00	03/2020 -	03/2024	136.19	48
168	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120	04/2008	3,503.69 -	5,912.40	2,161.74	03/2022 -	03/2024	68.75	24
	Total		1,35,577.71 -	2,66,058.71	138,110.53				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>								
169	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885	03/2016	160.27 -	213.97	25.64	08/2019 -	11/2022	33.51	39
170	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890	03/2018	217.22 -	226.88	170.96	08/2018 -	09/2021	4.45	37
171	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887	06/2016	236.78 -	263.26	65.84	08/2019 -	12/2021	11.18	28
172	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181	08/2010	186.96 -	322.24	298.52	09/2014 -	06/2021	72.36	81
173	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308	08/2010	193.69 -	327.92	301.46	10/2010 -	06/2021	69.30	128
174	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313	04/2013	166.27 -	359.92	243.59	08/2013 -	06/2021	116.47	94
175	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314	01/2013	182.28 -	369.64	274.07	02/2013 -	06/2021	102.79	100

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(April 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
176	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]	04/2013	151.59 -	370.01	281.74	08/2013 -	06/2021	144.09	94
177	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]	08/2010	195.04 -	377.99	331.49	10/2010 -	06/2021	93.80	128
178	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]	11/2017	392.33 -	428.55	351.92	03/2018 -	06/2021	9.23	39
179	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]	01/2016	476.20 544.00	544.00	400.38	09/2016 -	06/2021	14.24	57
180	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]	01/2016	497.14 -	572.66	270.56	08/2016 -	06/2021	15.19	58
181	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]	10/2013	445.89 653.00	653.29	754.40	03/2017 -	04/2021	46.51	49
182	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]	01/2016	624.98 -	731.50	416.16	10/2016 -	06/2021	17.04	56
183	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]	11/2013	497.05 -	881.05	754.27	05/2017 -	-	77.26	47
184	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]	11/2011	954.43 -	1,191.51	235.61	09/2015 -	10/2021	24.84	73
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
185	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]	03/2016	373.07 -	387.00	245.80	08/2016 -	05/2021	3.73	57
	<u>National Highways Authority Of India</u>								
186	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]	10/2015	593.26 -	690.17	595.33	05/2018 -	06/2021	16.34	37
187	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]	10/2015	531.13 -	730.97	653.06	05/2018 -	06/2021	37.63	37
188	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	03/2017	754.54 -	756.27	379.05	03/2020 -	12/2021	.23	21
189	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]	04/2017	894.00 -	929.32	810.00	04/2020 -	07/2021	3.95	15
190	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]	09/2017	1,124.11 -	1,232.76	527.67	09/2017 -	05/2021	9.67	44
191	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]	03/2017	1,288.07 -	1,420.00	842.24	03/2020 -	06/2021	10.24	15

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(April 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
192	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]	03/2018	1,532.62 -	2,499.00	761.73	03/2021 -	04/2021	63.05	1
193	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	3,182.34	3,087.00	04/2015 -	06/2021	65.04	74
194	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]	09/2011	2,848.00 -	3,379.45	2,901.20	03/2014 -	12/2022	18.66	105
	Total		17,445.14 -	23,041.67	15,979.69				
	<u>RURAL DEVELOPMENT</u>								
	<u>Hindustan Steelwork Construction Limited</u>								
195	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	03/2007	149.73 173.00	155.66	144.95	12/2015 -	10/2021	3.96	70
196	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]	12/2007	202.61 227.00	207.12	190.22	12/2016 -	10/2021	2.23	58
	Total		352.34 -	362.78	335.17				
	<u>STEEL</u>								
	<u>National Mineral Development Corporation (Nmdc)</u>								
197	NMDC INTEGRATED STEEL PLANT - [N12000086]	01/2010	15,525.00 -	21,940.00	18,516.49	05/2015 -	07/2021	41.32	74
	Total		15,525.00 -	21,940.00	18,516.49				
	<u>TELECOMMUNICATIONS</u>								
	<u>Department Of Telecommunication</u>								
198	NETWORK FOR SPECTRUM - [N26000101]	03/2012	13,334.00 -	24,664.00	17,845.00	07/2015 -	07/2021	84.97	72
	Total		13,334.00 -	24,664.00	17,845.00				
	<u>URBAN DEVELOPMENT</u>								
	<u>Ahmedabad Metro Rail</u>								
199	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]	11/2014	10,773.00 -	12,787.00	8,768.08	12/2018 -	08/2022	18.69	44
	<u>Bangalore Metro Rail Corporation Limited</u>								
200	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]	02/2014	26,405.14 -	30,695.12	17,021.86	02/2019 -	06/2024	16.25	64
	<u>Mumbai Metro Rail Corporation Ltd</u>								
201	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]	07/2013	23,136.00 -	33,406.00	17,039.36	01/2015 -	03/2023	44.39	98

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(April 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	Total		60,314.14 -	76,888.12	42,829.30				
	<u>WATER RESOURCES</u>								
	<u>Kolkata Metropolitan Development Authority</u>								
202	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]	05/2018	198.43 -	224.69	-	02/2022 -	06/2022	13.23	4
	<u>Polavaram Project Authority</u>								
203	POLAVARAM IRRIGATION PROJECT - [N30000002]	02/2009	10,151.04 -	55,548.87	17,325.20	03/2020 -	04/2022	447.22	25
	Total		10,349.47 -	55,773.56	17,325.20				
	Grand Total		4,84,045.63	7,93,538.96	486,762.75				

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Annexure - V

(April 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
	<u>Bhavini Limited</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,840.00	5,935.96	09/2010 -	10/2022	95.88
	<u>Nuclear Power Corporation Of India Limited</u>							
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	16,488.00	12/2015 -	02/2022	44.69
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]	10/2009	12,320.00 -	17,079.00	13,206.00	12/2016 -	03/2023	38.63
	Total		27,271.00 -	40,499.00	35,629.96			
	<u>CIVIL AVIATION</u>							
	<u>Airport Authority Of India Limited</u>							
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	417.23 -	707.73	379.95	09/2018 -	06/2021	69.63
5	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	07/2018	346.27 -	480.33	51.11	09/2021 -	09/2021	38.72
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI [N04000083]	12/2016	1,142.00 -	1,232.00	368.37	03/2021 -	03/2022	7.88
	Total		1,905.50 -	2,420.06	799.43			
	<u>COAL</u>							
	<u>Bharat Coking Coal Limited</u>							
7	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]	10/2015	243.00 -	334.27	18.35	04/2018 -	06/2022	37.56
8	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]	12/2015	304.13 -	341.22	40.84	03/2017 -	03/2022	12.20
	<u>Eastern Coal Fields Limited</u>							
9	RANIGANJ MASTER PLAN - [N06000163]	08/2009	2,661.73 -	5,146.48	621.70	08/2019 -	-	93.35
	<u>Neyveli Lignite Corporation</u>							
10	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	06/2011	5,907.11 -	7,980.79	7,405.84	12/2015 -	02/2021	35.10
11	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80	11,574.21	11/2021 -	07/2022	.00
	<u>Singareni Colliers Company Limited</u>							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
12	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	416.07	03/2012 -	03/2023	16.86
13	KAKATIYAKHANI OPENCASE-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	109.25	03/2019 -	03/2022	11.42
14	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 -	473.22	79.04	03/2015 -	03/2023	5.85
15	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	251.14	03/2015 -	03/2022	114.60
	<u>South-Eastern Coal Fields Limited</u>							
16	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	202.90	03/2015 -	03/2022	201.44
	<u>Western Coal Fields Limited</u>							
17	BHANEAGAN OC - [N06000121]	02/2015	187.94 -	409.68	86.81	03/2023 -	03/2023	117.98
18	NEW MAJRI UG TO OC - [N06000128]	05/2015	295.56 -	496.38	164.25	03/2019 -	09/2026	67.95
19	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	06/2015	483.69 -	499.00	252.15	03/2021 -	03/2021	3.17
20	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	08/2015	727.28 -	745.03	365.38	03/2025 -	03/2025	2.44
21	ADASA UG TO OC - [N06000133]	08/2015	288.90 -	333.43	142.27	03/2023 -	03/2024	15.41
22	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]	02/2016	198.68 -	325.18	253.17	03/2019 -	03/2022	63.67
23	BHATADI EXPANSION OC MINE - [N06000150]	02/2016	304.52 -	729.86	160.67	03/2019 -	09/2026	139.68
24	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	08/2016	319.76 -	404.45	246.02	03/2022 -	03/2022	26.49
25	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]	09/2016	289.29 -	289.30	35.95	03/2022 -	03/2025	.00
26	KOLAR PIMPRI EXTENSION OC - [N06000160]	03/2017	362.73 -	402.90	330.34	03/2020 -	09/2022	11.07
	Total		31,389.63 -	37,889.80	22,756.35			
	<u>DPIIT</u>							
	<u>Delhi Mumbai Industrial Corridor</u>							
27	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]	09/2011	12,579.09 -	13,812.30	8,915.05	09/2019 -	07/2021	9.80
	<u>India International Convention And Expo Centre</u>							
28	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]	11/2017	4,773.00 -	5,178.00	2,557.37	12/2019 -	12/2021	8.49
	Total		17,352.09 -	18,990.30	11,472.42			

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
	<u>HEALTH AND FAMILY WELFARE</u>							
	<u>Central Public Works Department</u>							
29	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]	03/2019	1,577.00 -	1,828.00	-	09/2025 -	09/2025	15.92
	<u>Hospital Services Consultancy Corporation Ltd</u>							
30	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	02/2013	414.11 -	499.23	494.72	11/2013 -	05/2021	20.55
31	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 -	250.00	240.24	05/2017 -	03/2021	22.29
32	AIIMS - OPD(NEW) - [N21000009]	08/2014	293.65 -	325.00	299.76	05/2017 -	01/2020	10.68
33	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]	12/2014	168.90 -	191.20	169.51	05/2017 -	07/2019	13.20
34	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	09/2014	505.58 -	585.00	586.96	03/2018 -	09/2019	15.71
35	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]	07/2016	152.95 -	177.92	164.17	02/2018 -	03/2021	16.33
36	CNCI KOLKATA WEST BENGAL - [N21000015]	08/2016	244.00 -	248.00	224.92	09/2018 -	05/2019	1.64
37	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	08/2017	272.19 -	272.54	272.54	03/2019 -	03/2021	.13
38	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]	12/2017	156.56 -	190.34	143.14	-	06/2021	21.58
39	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]	01/2018	249.01 -	249.07	231.05	-	01/2021	.02
	<u>National Building Construcion Corporation Ltd</u>							
40	AIIMS BILASPUR - [N21000028]	04/2018	1,351.00 -	1,471.00	712.04	09/2021 -	09/2021	8.88
	Total		5,589.39 -	6,287.30	3,539.05			
	<u>HOME AFFAIRS</u>							
	<u>Central Public Works Department</u>							
41	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	2,000.00	906.04	10/2019 -	12/2021	64.04
42	NSG AT KOLKATA - [N28000104]	10/2014	162.88 -	238.00	171.19	04/2018 -	12/2021	46.12
	Total		1,382.09 -	2,238.00	1,077.23			
	<u>HUMAN RESOURCE DEVELOPMENT</u>							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
43	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	224.58	06/2017 -	10/2021	.57
44	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]	08/2016	294.00 -	350.69	276.69	04/2019 -	05/2021	19.28
45	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]	12/2016	549.31 -	559.47	458.38	07/2019 -	-	1.85
46	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133]	02/2019	186.00 199.00	205.00	130.63	09/2020 -	-	10.22
	<u>Rail India Technical And Economic Service</u>							
47	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]	09/2013	484.32 -	626.26	-	09/2014 -	-	29.31
	Total		2,009.81 -	2,240.41	1,090.28			
	<u>PETROLEUM</u>							
	<u>Bharat Petroleum Corporation Limited</u>							
48	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29 -	5,245.96	5,076.00	08/2018 -	05/2021	14.33
49	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]	11/2012	678.00 -	1,472.00	19.44	02/2017 -	08/2022	117.11
50	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]	12/2015	1,112.00 -	1,507.24	730.00	06/2019 -	02/2022	35.54
	<u>Gas Authority Of India Limited</u>							
51	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]	06/2009	2,915.00 2,915.00	5,909.00	3,607.20	12/2012 -	02/2022	102.71
52	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	04/2017	287.49 -	345.15	200.77	04/2022 -	04/2022	20.06
53	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]	09/2018	225.54 -	247.90	40.10	02/2021 -	12/2021	9.91
54	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]	08/2018	286.42 -	327.01	186.00	08/2020 -	06/2021	14.17
	<u>Hindustan Petroleum Corporation Limited</u>							
55	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	07/2016	20,928.00 -	26,264.00	14,820.38	07/2020 -	07/2022	25.50
56	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]	09/2015	4,199.00 -	5,060.00	4,528.82	03/2020 -	-	20.50
57	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	09/2017	2,677.00 -	3,072.00	2,239.96	06/2021 -	08/2022	14.76

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
58	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA [N16000312]	11/2017	255.00 -	300.00	271.70	11/2020 -	06/2021	17.65
	<u>Indian Oil Corporation Limited</u>							
59	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	1,236.00	394.74	10/2017 -	03/2022	103.60
60	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	01/2015	1,823.00 -	3,027.90	1,957.55	03/2021 -	12/2021	66.09
61	PARADIP HYDERABAD PIPELINE - [N16000194]	01/2015	2,321.00 -	3,338.00	2,923.70	12/2020 -	03/2022	43.82
62	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]	06/2016	423.00 -	502.00	422.12	08/2019 -	06/2021	18.68
63	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	05/2016	4,497.00 -	6,025.00	3,681.97	12/2018 -	02/2022	33.98
64	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]	08/2017	236.00 -	293.00	161.05	06/2020 -	09/2021	24.15
65	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT [N16000336]	03/2018	588.20 -	730.20	77.30	- -	05/2023	24.14
	<u>Mangalore Refinery And Petrochemicals Limited</u>							
66	SEA WATER DESALINATION PLANT - [N16000319]	11/2017	581.00 -	637.00	489.10	03/2020 -	07/2021	9.64
	<u>Oil & Natural Gas Corporation Limited</u>							
67	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) [N16000128]	03/2011	861.79 -	2,001.00	1,551.48	05/2013 -	02/2022	132.19
68	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS [N16000213]	12/2015	3,190.69 -	3,375.90	2,786.78	04/2018 -	05/2022	5.80
69	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	823.27 -	1,137.79	669.73	03/2023 -	03/2022	38.20
70	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	07/2016	249.85 250.00	303.75	199.31	05/2020 -	05/2021	21.57
71	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]	04/2019	3,228.80 -	3,976.67	1,188.33	03/2022 -	05/2023	23.16
72	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]	05/2019	3,660.71 -	3,740.05	2,808.52	05/2021 -	01/2022	2.17
	<u>Oil India Limited</u>							
73	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	490.24	455.00	03/2017 -	-	39.05

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
74	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	01/2018	543.91 -	652.10	320.30	02/2020 -	06/2021	19.89
	Total		62,139.58 -	81,216.86	51,807.35			
	<u>POWER</u>							
	<u>National Hydro-Electric Power Corporation</u>							
75	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	9,897.59	8,945.10	09/2009 -	07/2022	152.52
76	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	19,992.43	13,732.39	09/2010 -	08/2023	218.08
	<u>National Thermal Power Corporation</u>							
77	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	15,105.22	13,657.43	01/2018 -	-	29.79
78	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	5,867.38	4,913.02	03/2013 -	12/2022	96.99
79	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	09/2014	9,188.98 -	9,842.02	7,391.78	07/2019 -	03/2021	7.11
80	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 -	13,140.91	11,730.23	12/2018 -	05/2021	4.86
81	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,389.42	11,722.10	06/2019 -	10/2022	7.12
82	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	10,566.00	8,847.06	07/2012 -	07/2021	97.38
83	NPCCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	17,304.00	15,787.92	05/2018 -	12/2021	33.47
84	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]	04/2012	9,750.89 -	12,176.28	11,130.00	02/2017 -	-	24.87
85	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	21,312.11	18,595.56	10/2011 -	07/2023	145.16
86	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	13,766.78	10/2017 -	-	7.55
87	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	07/2012	1,527.00 -	1,801.07	149.21	08/2017 -	-	17.95
88	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	03/2015	9,870.51 -	11,148.86	10,019.31	01/2020 -	-	12.95
89	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	01/2016	10,598.98 -	10,997.70	8,368.64	11/2020 -	07/2022	3.76
90	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	3,601.54	10/2017 -	-	7.41
	<u>North East Electric Power Corporation</u>							
91	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	7,927.34	8,225.88	12/2009 06/2016	-	217.49
	<u>Power Grid Corporation Of India Limited</u>							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
92	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]	10/2008	4,824.12 -	5,071.94	4,634.56	10/2012 -	03/2021	5.14
93	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	14,719.10	12,894.95	08/2013 -	08/2022	32.24
94	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	1,326.81	04/2016 -	07/2020	38.61
95	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	546.36	478.29	11/2016 -	06/2021	4.61
96	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]	01/2015	871.62 -	902.49	648.77	10/2017 -	01/2021	3.54
97	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03	200.16	07/2017 -	-	27.92
98	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	590.30	06/2014 -	-	31.17
99	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]	10/2016	408.46 -	516.12	417.12	01/2019 -	04/2020	26.36
100	COMPREHENSIVE SCHEME FOR THE STRENGHTENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,129.32	2,163.30	12/2018 -	03/2024	92.02
101	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,700.00	2,767.14	12/2018 -	12/2021	31.08
102	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	03/2017	3,500.00 3,500.00	3,994.00	2,917.31	07/2020 -	06/2021	14.11
103	TRANSMISSION SYSTEM FOR EVACUTION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]	05/2017	186.17 -	219.66	157.20	07/2019 -	06/2021	17.99
104	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]	05/2017	445.89 -	675.73	463.08	02/2019 -	02/2021	51.55
	<u>Satluj Jal Vidyut Nigam Limited</u>							
105	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	947.89	577.17	12/2021 -	12/2021	46.20
	<u>Thdc India Limited</u>							
106	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,860.35	2,223.06	06/2013 -	12/2023	54.94
	Total		1,75,198.45 -	2,49,834.01	203,043.17			
	<u>RAILWAYS</u>							
	<u>Central Railways</u>							
107	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89 -	1,377.48	335.23	03/2021 -	03/2023	73.73

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
108	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 -	315.00	312.62	03/2019 -	-	71.14
109	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 -	4,517.49	2,648.51	03/2021 -	03/2023	98.88
110	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024	120.28
111	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 -	3,438.51	-	03/2024 -	03/2024	25.04
112	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	1,272.19 -	1,283.49	408.70	03/2022 -	03/2023	.89
113	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	445.15	03/2023 -	03/2023	10.94
	<u>Container Corporation Of India</u>							
114	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]	01/2013	387.70 -	487.13	434.63	03/2018 -	-	25.65
115	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 -	235.00	14.14	03/2019 -	-	.21
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>							
116	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]	10/2006	11,589.00 30,357.00	28,181.00	-	- -	-	143.17
117	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	-	207.99
	<u>East Central Railways</u>							
118	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	03/1999	1,033.07 -	3,550.00	3,567.20	- -	03/2022	243.64
119	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	04/2003	528.65 -	2,066.78	1,560.44	- -	03/2023	290.95
120	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	477.88 283.95	751.55	694.88	03/2012 -	07/2021	57.27
121	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	324.73 -	1,070.00	1,069.58	03/2012 -	11/2022	229.50
122	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	614.45	348.95	- -	12/2023	277.26
123	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	499.41 -	516.02	447.86	03/2020 -	-	3.33
124	SAMASTIPUR-DARBANGHA - [N22000329]	05/2015	380.00 -	519.33	282.65	- -	03/2025	36.67
125	HAJIPUR - BACHAWARA - [N22000334]	05/2015	678.54 -	929.86	848.39	03/2019 -	05/2021	37.04
126	KODERMA-TILAIYA (NL), ECR - [220100305]	04/2002	459.91 -	1,625.87	758.44	- -	03/2023	253.52
127	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 -	549.75	15.58	- -	-	32.26
128	BIHTA-AURANGABAD (NL) - [N22000170]	04/2008	326.20 -	2,995.01	2.08	- -	03/2024	818.15

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
129	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	325.00 -	735.20	384.25	- -	03/2021	126.22
130	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	378.56 -	1,858.75	386.35	- -	03/2023	391.01
131	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	1,006.00	24.16	- -	-	376.78
132	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) [N22000180]	04/2004	372.14 -	1,470.50	1,288.24	- -	03/2023	295.15
133	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC [N22000181]	04/2009	548.00 -	819.01	535.44	03/2020 -	03/2023	49.45
134	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	480.00	486.66	- -	-	125.34
135	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	546.71	541.43	07/2014 -	-	64.60
136	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 -	1,215.54	426.72	03/2021 -	03/2024	63.37
137	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 -	1,185.73	217.95	03/2021 -	06/2022	62.06
138	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]	04/1998	180.82 -	726.31	546.29	- -	-	301.68
139	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]	04/1991	329.39 -	1,483.14	1,207.52	- -	03/2022	350.27
	<u>East Coast Railway</u>							
140	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07	873.81	06/2021 -	03/2025	137.80
141	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	2,923.13 -	3,791.66	1,506.95	03/2009 -	03/2026	29.71
142	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	1,111.99 -	1,539.28	1,109.06	02/2019 -	12/2021	38.43
143	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,160.83	950.18	03/2020 -	03/2023	.07
144	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 -	238.03	221.48	03/2020 -	03/2022	52.77
145	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE [N22000380]	04/2015	701.61 -	810.02	171.45	11/2018 -	03/2024	15.45
	<u>Eastern Railways</u>							
146	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,619.48	905.06	03/2019 12/2009	03/2025	36.22
147	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 -	1,425.44	638.05	02/2013 -	03/2024	134.80
148	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]	04/2010	365.17 -	439.30	411.65	03/2017 -	03/2025	20.30

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
149	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 -	527.54	1.76	-	03/2025	44.46
150	HANSDIHA-GODDA NL - [N22000236]	04/2011	542.18 -	663.13	534.85	03/2020	03/2021	22.31
151	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]	04/2011	175.80 -	495.10	288.51	-	03/2022	181.63
152	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	04/2011	299.60 -	335.62	1.12	03/2017	03/2026	12.02
153	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]	04/2010	494.54 -	494.59	32.00	03/2005	03/2025	.01
154	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]	04/2000	297.47 -	298.22	52.09	-	03/2025	.25
155	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHNACHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	499.96 -	680.68	164.09	02/2012	03/2025	36.15
156	MONIGRAM- NIMTITA - [N22000301]	04/2012	250.93 -	310.70	293.10	-	03/2024	23.82
157	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	04/2012	255.64 -	272.20	261.26	-	03/2022	6.48
158	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]	04/1987	406.99 -	545.70	149.31	03/2006	03/2025	34.08
159	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]	04/2007	450.00 -	1,261.34	-	-	03/2025	180.30
160	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 -	260.10	11.74	-	03/2025	51.19
161	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	2,137.81	388.53	03/2022	03/2025	133.39
162	BANDEL-BOINCHI 3RD LINE - [N22000221]	04/2011	288.35 -	502.48	432.62	-	03/2021	74.26
163	PIRPAINTI-BHAGALPUR - [N22000222]	04/2011	261.38 -	565.00	547.01	-	05/2019	116.16
164	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]	04/2001	923.52 -	995.10	645.97	03/2016	03/2025	7.75
165	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]	04/2005	595.51 -	769.40	103.86	03/2017	03/2025	29.20
<u>Indian Railway Construction Company Limited</u>								
166	GEVRA ROAD PENDRA ROAD - [N22000488]	02/2014	2,288.00 -	4,970.11	866.16	03/2022	12/2023	117.23
167	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]	04/2013	3,055.00 -	3,055.15	2,431.72	09/2018	03/2022	.00
<u>Metropolitan Rapid Transport Projects</u>								

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
168	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69 -	3,404.92	3,837.57	12/2006 -	-	224.37
169	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	2,980.41	1,768.25	03/2004 -	03/2022	501.57
170	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028	04/2006	495.74 -	734.01	510.69	06/2013 -	12/2021	48.06
171	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	75.91
	<u>North Central Railway</u>							
172	ETAWAH-MAINPURI (NL),NCR - [220100318	04/1997	120.00 -	346.00	345.51	12/2008 -	-	188.33
173	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	04/2011	2,912.96 -	3,845.60	148.26	03/2022 -	12/2024	32.02
174	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372	04/2015	668.70 668.00	680.00	330.00	03/2020 -	-	1.69
	<u>North East Frontier Railway</u>							
175	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135	04/1983	297.32 -	614.00	275.06	03/2019 -	-	106.51
176	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	2,393.47 -	5,521.45	3,954.28	03/2014 -	03/2023	130.69
177	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	1,180.19 -	4,541.38	3,804.55	12/2008 -	05/2021	284.80
178	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	4,454.17 -	12,264.15	10,994.55	03/2011 -	12/2023	175.34
179	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086	09/2006	385.20 -	1,043.00	837.67	03/2019 -	03/2023	170.77
180	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087	09/2006	532.87 -	2,145.00	1,001.65	03/2019 -	03/2024	302.54
181	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124	04/2006	2,326.52 -	6,911.00	1,204.64	03/2015 -	12/2024	197.05
182	KISHANGANJ JALALGARH, NL, NEFR - [N22000101	04/2008	333.76 -	360.00	6.74	- -	-	7.86
183	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	8,600.00	619.18	12/2015 -	-	542.04
184	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183	04/2013	1,798.00 -	2,042.51	136.41	03/2019 -	03/2024	13.60
185	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193	04/2010	221.42 -	380.00	38.20	- -	-	71.62
186	AGARTALA-AKHAURA NL - [N22000195	04/2012	569.63 -	742.00	200.28	03/2020 -	03/2022	30.26
187	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205	04/2010	906.46 -	4,083.02	264.33	03/2021 -	-	350.44

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
188	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00	76.56	03/2020 -	-	94.45
189	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	373.87	287.09	-	12/2021	54.80
190	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84 -	1,040.00	156.54	03/2020 -	-	150.70
191	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	04/1999	819.23 -	1,871.00	1,082.01	-	-	128.39
192	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	314.00 -	800.00	823.02	03/2019 -	03/2021	154.78
193	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	04/2015	2,232.32 -	2,950.00	1,620.12	03/2022 -	03/2023	32.15
194	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 -	1,873.21	1,309.41	03/2021 -	05/2021	115.07
195	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	04/2016	602.27 -	2,144.78	921.83	12/2021 -	04/2021	256.12
196	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]	02/1999	380.60 -	1,090.60	1,089.12	04/2010 -	-	186.55
	<u>North Eastern Railway</u>							
197	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	142.45 -	228.40	0.15	-	-	60.34
198	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	-	-	-	8.10
199	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 -	1,409.09	-	-	-	358.99
200	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 -	895.00	111.89	12/2021 -	12/2021	267.13
201	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	378.98	01/2019 -	02/2022	61.80
202	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 -	644.00	-	-	-	.16
203	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	12.86	04/2016 -	12/2021	.16
204	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]	04/2017	1,343.00 -	1,476.15	-	01/2018 -	-	9.91
205	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]	04/2016	602.50 -	714.34	40.34	-	12/2023	18.56
	<u>North Western Railway</u>							
206	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	860.41	709.62	02/2019 -	06/2022	109.82
207	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	701.81	236.13	03/2020 -	10/2022	16.97

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
208	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL [N22000330]	05/2015	873.71 -	1,980.21	4.60	- -	-	126.64
209	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	395.00	348.47	12/2019 -	02/2021	60.52
210	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	4,262.36	186.12	- -	-	104.65
211	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	350.45	273.79	10/2018 -	01/2020	47.91
212	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]	04/2013	822.00 -	1,099.00	-	- -	-	33.70
213	PUSHKAR-MERTA - [N22000151]	04/2013	323.00 -	432.22	-	- -	-	33.81
214	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTISURGARH-UDAIPUR [N22000152]	04/2013	420.18 -	480.00	357.41	03/2020 -	06/2021	14.24
215	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	375.00	348.55	11/2019 -	03/2021	75.73
216	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	525.00	460.83	02/2019 -	02/2020	116.86
	<u>Northern Railway</u>							
217	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	359.00	111.51	- -	03/2024	129.17
218	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	893.45	705.53	12/2011 -	06/2021	211.31
219	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]	04/2007	336.91 -	791.39	572.99	- -	03/2023	134.90
220	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]	04/2012	295.68 -	419.00	127.91	- -	09/2023	41.71
221	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63	204.53	- -	-	57.68
222	UNCHAHAH-AMETHI - [N22000294]	04/2012	1,229.00 -	1,265.00	103.72	- -	03/2023	2.93
223	QADIAN-BEAS - [N22000295]	04/2011	205.22 -	841.90	1.73	- -	03/2024	310.24
224	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,200.00	714.78	07/2012 -	03/2024	388.89
225	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	27,949.00	24,040.61	11/2002 -	12/2022	1,017.96
226	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 -	1,540.13	242.04	03/2023 -	03/2025	369.35
227	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 -	859.00	852.73	03/2016 -	06/2021	37.44
	<u>Rail Vikas Nigam Ltd.</u>							
228	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	1,185.64 -	1,844.47	1,883.44	12/2017 -	-	55.57

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
229	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	1,202.70 -	2,440.53	1,337.54	02/2015 -	06/2022	102.92
230	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	396.00	388.21	03/2009 03/2009	-	196.83
231	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111	04/2010	2,913.51 -	4,639.00	1,119.31	03/2016 -	03/2025	59.22
232	BHANUPALI-BILASPUR BERI NL - [N22000273	04/2008	2,966.99 -	6,753.42	926.84	12/2026 -	12/2025	127.62
233	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297	04/2010	2,127.00 -	3,000.00	2,208.46	03/2023 -	12/2022	41.04
234	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110	04/2010	3,951.98 -	4,259.48	2,734.83	03/2016 -	03/2025	7.78
235	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109	04/2010	2,298.42 -	2,733.86	40.46	03/2014 -	12/2025	18.95
236	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313	03/2012	1,503.71 -	3,377.00	2,683.67	03/2020 -	03/2022	124.58
237	AHMEDABAD-BOTAD (GC) - [N22000140	04/2012	975.62 -	1,500.00	1,497.74	12/2021 -	12/2021	53.75
238	DHASA-JETALSAR (GC) - [N22000141	04/2012	644.38 -	872.65	800.30	03/2021 -	03/2021	35.42
239	PALANPUR-SAMAKHAYALI (DL) - [N22000144	04/2013	1,548.66 -	1,868.89	1,831.45	12/2021 -	03/2022	20.68
240	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213	04/2012	632.68 -	950.00	810.96	03/2016 -	12/2021	50.15
241	VIJAYAWADA-GUDUR - [N22000369	04/2015	3,246.26 -	3,548.68	2,224.17	12/2023 -	12/2023	9.32
242	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401	04/2015	943.60 -	1,000.00	688.03	03/2022 -	12/2024	5.98
243	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403	04/2015	773.94 -	850.00	705.50	12/2024 -	12/2024	9.83
244	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404	04/2011	927.01 -	1,400.00	1,331.76	03/2019 -	06/2022	51.02
245	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406	04/2011	16,216.00 -	22,716.11	2,997.71	12/2024 -	03/2025	40.08
246	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407	03/2009	713.48 -	2,725.00	2,554.71	03/2020 -	12/2021	281.93
247	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409	01/1991	2,335.67 -	3,327.72	1,317.36	12/2024 -	12/2026	42.47
248	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410	03/2006	948.04 -	2,009.00	1,875.48	03/2020 -	12/2021	111.91
249	BANASPAHI - JAKHPURA - DOUBLING - [N22000412	03/2009	942.95 -	1,536.00	1,089.84	03/2019 -	06/2022	62.89

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
250	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	03/2012	1,183.25 -	1,825.00	1,411.49	12/2020 -	12/2022	54.24
251	BINA - KOTA DOUBLING WITH RE - [N22000414]	04/2011	1,485.85 -	1,835.83	1,571.35	12/2020 -	12/2021	23.55
	<u>Railway Electrification</u>							
252	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	141.55	03/2012 -	-	60.77
	<u>South Central Railway</u>							
253	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 -	2,120.16	883.52	03/2009 -	03/2024	102.85
254	MANUGURU-RAMAGUNDAM - [N22000259]	04/2013	1,112.00 -	2,911.84	0.92	- -	-	161.86
255	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,856.95 -	1,952.68	567.51	03/2023 -	03/2024	5.16
256	NADIKUDE-SRI KALAHASTI - [N22000286]	04/2011	2,288.70 -	2,643.25	1,231.85	03/2021 -	03/2024	15.49
257	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	704.31 -	927.94	534.34	03/2020 -	06/2021	31.75
258	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]	04/2008	2,132.77 -	3,037.95	350.54	03/2014 -	03/2027	42.44
259	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	164.36 -	1,050.00	999.64	02/2009 -	-	538.84
260	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	1,723.00 1.00	3,421.35	1,895.77	03/2000 -	03/2023	98.57
261	GUNTUR-GUNTAKAL - [N22000368]	04/2016	3,631.00 -	3,887.48	1,144.64	03/2022 -	03/2024	7.06
262	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	04/2017	119.73 185.00	449.39	7.09	03/2022 -	12/2022	275.34
	<u>South East Central Railway</u>							
263	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	1,413.76	1,416.77	- -	-	268.37
264	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	511.86 -	2,005.25	1,777.22	04/2020 -	-	291.76
265	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,908.51 -	3,524.81	982.38	03/2023 -	12/2023	84.69
266	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]	04/2010	585.93 -	1,268.32	941.56	02/2019 -	12/2021	116.46
267	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00 -	1,096.00	39.79	12/2021 -	12/2024	378.60
268	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]	04/2008	872.00 -	1,226.51	1,131.91	12/2019 -	-	40.65
269	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	04/2015	1,973.00 -	2,135.34	351.35	03/2021 -	12/2023	8.23

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
270	ANUPPUR-KATNI - [N22000485]	04/2015	1,370.00 -	1,370.94	470.49	12/2021 -	12/2023	.07
	<u>South Eastern Railway</u>							
271	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00	182.49	03/2007 03/2007	-	160.76
272	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	377.00	201.09	12/2016 -	08/2020	153.41
273	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	620.00	40.99	- -	03/2025	131.89
274	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	651.00 -	1,009.00	7.96	03/2015 -	03/2025	54.99
275	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	54.46	03/2015 -	-	53.44
276	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	358.68	314.33	12/2018 -	04/2021	38.92
277	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	1,312.96	940.00	03/2020 -	12/2021	35.38
278	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 -	2,373.00	485.04	03/2003 -	03/2030	130.97
	<u>South Western Railway</u>							
279	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	1,801.01 -	1,967.00	71.56	- -	12/2023	9.22
280	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	296.10	0.01	- -	12/2023	.03
281	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	2,062.30 -	2,432.50	1,127.71	- -	03/2025	17.95
282	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	0.34	- -	12/2023	14.14
283	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	2,315.00 -	3,911.65	157.01	- -	12/2024	68.97
284	HUBLI- CHIKJAJUR - [N22000325]	03/2015	1,156.94 -	1,656.00	1,160.49	03/2020 -	03/2023	43.14
285	YELAHANKA-PENUKONDA - [N22000328]	05/2015	860.43 -	1,147.00	911.86	03/2020 -	06/2021	33.31
286	ARSIKERE-TUMKUR - [N22000332]	03/2015	578.00 -	783.00	620.29	03/2020 -	06/2021	35.47
287	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 -	1,870.41	1,341.15	03/2019 -	03/2024	15.84
288	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78 -	998.00	463.45	03/2017 -	03/2025	54.78
	<u>Southern Railway</u>							
289	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY'-AGASTIYAMPALLI [N22000079]	09/2007	724.69 -	2,910.84	1,621.40	02/2019 -	03/2025	301.67
290	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	303.98 -	1,720.00	701.37	03/2020 -	03/2025	465.83

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
291	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	1,566.00 -	2,815.62	262.68	-	-	79.80
292	ATTIPPATTU PUTTUR - [N22000184	04/2008	151.84 -	527.37	2.59	02/2019	-	247.32
293	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185	04/2008	523.52 -	1,205.00	2.28	-	03/2024	130.17
294	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186	04/2013	839.00 -	1,500.00	0.63	-	-	78.78
295	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187	04/1999	198.68 -	559.95	52.50	-	03/2024	181.84
296	KURUPPANTHARA-CHINGAVANAM - [N22000190	04/2007	270.14 -	457.08	439.49	-	12/2021	69.20
297	KUMBALAM-TURAVUR - [N22000191	04/2011	252.96 -	369.55	8.50	-	-	46.09
298	ERODE-PALANI - [N22000199	04/2008	288.57 -	1,140.00	1.63	-	-	295.05
299	MADURAI-BODINAYAKKANUR - [N22000201	04/2008	164.41 -	608.13	375.67	-	09/2021	269.89
300	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202	04/2007	931.98 -	1,121.00	928.75	-	05/2021	20.28
301	ERNAKULAM-KUMBALAM - [N22000204	04/2010	189.24 -	275.21	6.73	-	-	45.43
302	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215	04/2011	120.70 -	2,172.16	262.36	03/2019	12/2027	1,699.64
303	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373	10/2013	187.26 -	327.00	268.75	04/2014	-	74.62
304	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400	02/2015	1,000.00 -	1,246.00	0.81	-	-	24.60
305	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441	02/1996	268.87 -	950.00	928.36	03/2005	09/2021	253.33
306	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451	02/2015	760.00 -	1,536.00	1,233.08	03/2020	06/2022	102.11
<u>West Central Railway</u>								
307	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314	04/2001	424.60 -	2,909.99	1,229.79	03/2021	03/2023	585.35
308	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	247.66 -	8,248.50	2,131.17	05/2008	03/2025	3,230.57
309	KATNI GRADE SEPARATOR/BYE PASS - [N22000416	08/2016	582.13 -	1,247.64	296.69	03/2022	03/2023	114.32
<u>Western Railway</u>								
310	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120	04/2008	3,503.69 -	5,912.40	2,161.74	03/2022	03/2024	68.75

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
311	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]	04/2006	117.36 196.95	202.35	809.40	03/2011 -	-	72.42
312	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	411.62	126.05	03/2012 -	03/2023	29.34
313	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	04/2008	829.74 -	1,959.74	1,799.00	03/2020 -	03/2024	136.19
314	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	1,378.11	540.09	03/2019 -	03/2023	329.77
315	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	1,037.15 -	1,389.05	1,125.73	03/2021 -	12/2021	33.93
316	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]	02/1991	551.51 -	890.76	745.11	03/2019 -	10/2021	61.51
317	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]	04/2017	691.84 -	1,017.91	719.56	03/2020 -	02/2021	47.13
	Total		2,29,432.02 -	4,78,447.32	209,164.08			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>							
318	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]	12/2011	156.26 227.00	247.95	175.00	- -	-	58.68
319	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]	11/2010	624.41 -	992.67	890.74	03/2011 -	-	58.98
320	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]	12/2011	156.63 276.00	276.00	-	02/2012 -	-	76.21
321	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]	08/2010	193.69 -	327.92	301.46	10/2010 -	06/2021	69.30
322	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]	03/2012	207.03 -	389.45	308.09	05/2012 -	-	88.11
323	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]	04/2013	151.59 -	370.01	281.74	08/2013 -	06/2021	144.09
324	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]	04/2013	166.27 -	359.92	243.59	08/2013 -	06/2021	116.47
325	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]	01/2013	182.28 -	369.64	274.07	02/2013 -	06/2021	102.79

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
326	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]	03/2015	258.97 -	268.92	223.10	08/2015 -	-	3.84
327	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]	03/2015	157.18 162.00	162.00	146.79	07/2015 -	-	3.07
328	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]	03/2015	280.16 -	290.59	219.47	- -	-	3.72
329	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	01/2014	255.75 348.00	348.43	290.12	09/2017 -	-	36.24
330	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]	10/2013	445.89 -	653.29	464.05	03/2017 -	-	46.51
331	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]	11/2013	497.05 -	881.05	754.27	05/2017 -	-	77.26
332	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]	11/2010	268.08 -	390.73	283.52	05/2017 -	-	45.75
333	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]	11/2015	889.24 -	904.82	754.06	- -	-	1.75
334	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]	11/2010	470.20 -	630.36	386.98	02/2011 -	-	34.06
335	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]	01/1991	282.41 -	322.01	327.21	08/2016 -	-	14.02
336	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]	11/2011	954.43 -	1,191.51	235.61	09/2015 -	10/2021	24.84
337	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]	01/1991	358.22 -	377.64	339.86	10/2016 -	-	5.42
338	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]	10/2015	333.21 -	353.89	256.11	11/2015 -	-	6.21
339	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]	08/2010	195.04 -	377.99	331.49	10/2010 -	06/2021	93.80
340	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]	01/1991	319.68 -	369.77	249.55	- -	-	15.67
341	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]	03/2014	191.50 192.00	192.00	136.19	05/2016 -	-	.26

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
342	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]	08/2013	171.96 172.00	172.00	88.30	06/2016 -	-	.02
343	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]	03/2018	460.73 -	461.00	-	- -	-	.06
344	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]	11/2017	237.80 -	238.00	7.48	11/2019 -	-	.08
345	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O - [N24000871]	08/2014	600.87 720.97	720.97	682.36	11/2017 -	-	19.99
346	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873]	08/2014	823.20 937.76	937.76	807.99	11/2017 -	-	13.92
347	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]	03/2018	166.21 -	173.41	141.65	08/2018 -	-	4.33
348	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]	03/2016	160.27 -	213.97	25.64	08/2019 -	11/2022	33.51
349	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]	06/2016	236.78 -	263.26	65.84	08/2019 -	12/2021	11.18
350	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]	04/2014	279.70 398.22	398.22	322.91	08/2017 -	02/2020	42.48
351	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]	03/2018	217.22 -	226.88	170.96	08/2018 -	09/2021	4.45
352	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DSIGN CH0.0) TO KM 275/622(DSIGN CH 5.12 - [N24000928]	10/2015	333.21 -	355.89	315.57	12/2015 -	-	6.81
353	BHOKAR TO SARSAM - [N24001128]	02/2017	295.09 -	295.99	169.64	07/2019 -	-	.31
354	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]	10/2013	445.89 653.00	653.29	754.40	03/2017 -	04/2021	46.51
355	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]	11/2017	392.33 -	428.55	351.92	03/2018 -	06/2021	9.23
356	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]	08/2010	186.96 -	322.24	298.52	09/2014 -	06/2021	72.36
357	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]	09/2011	1,979.00 -	2,036.90	1,237.25	- -	-	2.93
358	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]	01/2016	497.14 -	572.66	270.56	08/2016 -	06/2021	15.19

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
359	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219	01/2016	476.20 544.00	544.00	400.38	09/2016 -	06/2021	14.24
360	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221	01/2016	624.98 -	731.50	416.16	10/2016 -	06/2021	17.04
361	WIDENING OF SL TO 2 L KM. 107-184.80 SUKUMA TO KONTA ON NH 221 - [N24001223	03/2010	179.89 271.00	271.00	270.91	03/2013 -	-	50.65
362	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1 - [N24001225	12/2010	169.26 299.00	299.00	-	01/2019 -	-	76.65
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>							
363	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676	12/2016	138.93 155.00	155.00	79.91	01/2017 -	-	11.57
364	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679	02/2017	195.23 -	252.79	102.51	04/2017 -	-	29.48
365	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680	02/2017	203.36 -	263.31	117.81	04/2017 -	-	29.48
366	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681	01/2017	194.66 -	252.05	113.63	04/2017 -	-	29.48
367	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686	03/2016	373.07 -	387.00	245.80	08/2016 -	05/2021	3.73
368	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690	01/2017	198.22 -	252.05	113.63	04/2017 -	-	27.16
369	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695	04/2017	388.00 -	447.37	261.20	10/2017 -	-	15.30
370	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902	10/2017	818.00 -	887.68	151.62	- -	-	8.52
	<u>National Highways Authority Of India</u>							
371	HARANGAJAO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 -	520.00	612.58	02/2009 -	-	85.71
372	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	340.14	325.28	04/2009 -	-	70.23
373	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279	12/2003	167.64 -	435.78	427.96	11/2008 -	-	159.95
374	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	255.23	251.39	11/2008 -	-	64.62
375	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049	12/2003	160.00 -	167.98	233.27	05/2008 -	06/2019	4.99

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
376	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	655.17	655.17	07/2009 -	-	234.27
377	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,967.50	3,996.01	11/2011 -	-	167.82
378	INDORE-DEWAS(NH-3) - [N24000159]	11/2010	325.00 -	475.00	469.54	05/2013 -	-	46.15
379	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61 -	360.84	489.84	04/2010 -	07/2019	65.82
380	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 -	230.00	370.56	04/2008 -	02/2021	10.58
381	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	04/2014	1,266.60 -	1,544.00	1,446.45	09/2016 -	-	21.90
382	NASHRI- CHANANI - [N24000162]	05/2011	2,159.00 -	2,519.00	4,709.65	06/2015 -	-	16.67
383	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]	09/2011	2,848.00 -	3,379.45	2,901.20	03/2014 -	12/2022	18.66
384	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]	05/2011	511.54 -	591.00	575.99	11/2013 -	01/2021	15.53
385	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]	07/2012	291.36 -	469.31	459.07	01/2014 -	12/2020	61.08
386	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	3,182.34	3,087.00	04/2015 -	06/2021	65.04
387	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]	04/2014	351.34 -	417.68	433.68	01/2016 -	12/2020	18.88
388	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]	04/2014	495.78 -	627.93	633.24	01/2016 -	01/2020	26.66
389	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]	10/2015	531.13 -	730.97	653.06	05/2018 -	06/2021	37.63
390	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]	10/2015	361.15 -	363.93	272.98	- -	-	.77
391	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]	10/2015	593.26 -	690.17	595.33	05/2018 -	06/2021	16.34
392	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]	06/2015	845.24 -	941.00	889.83	- -	-	11.33
393	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]	12/2015	1,083.00 -	1,827.15	2,082.19	06/2018 -	-	68.71
394	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]	08/2015	814.04 -	825.17	512.04	- -	10/2021	1.37
395	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	05/2013	1,055.00 -	1,601.77	1,393.40	11/2015 -	-	51.83
396	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]	10/2015	447.29 -	746.43	676.33	12/2017 -	-	66.88

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
397	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]	01/1991	642.41 -	681.67	400.60	- -	-	6.11
398	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]	12/2015	1,167.45 -	1,182.94	186.70	- -	-	1.33
399	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]	04/2014	1,665.00 -	2,360.65	4,472.01	- -	-	41.78
400	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]	08/2015	854.80 -	1,038.56	1,160.00	- -	-	21.50
401	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]	08/2015	516.13 -	649.27	712.15	04/2018 -	-	25.80
402	MEERUT-BULANDSHAHAH - [N24000539]	01/2016	683.24 -	987.94	867.27	- -	-	44.60
403	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]	02/2016	997.15 -	1,115.95	975.08	03/2019 -	-	11.91
404	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH- 29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]	03/2016	1,587.49 -	2,982.00	276.87	04/2019 -	-	87.84
405	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]	05/2016	364.56 -	392.00	353.42	- -	04/2021	7.53
406	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]	07/2016	458.03 -	486.00	432.16	- -	-	6.11
407	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]	08/2016	1,388.34 -	2,587.50	1,569.38	09/2019 -	-	86.37
408	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]	08/2016	1,169.61 -	2,280.00	1,282.04	- -	-	94.94
409	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]	08/2016	323.72 -	336.60	312.79	08/2018 -	-	3.98
410	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]	09/2016	1,239.82 -	1,727.66	1,674.80	- -	-	39.35
411	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH- 209(EXISTING CHAINAGE FROM - [N24000622]	09/2016	950.69 -	1,108.00	1,429.25	08/2019 -	-	16.55
412	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]	09/2016	1,100.19 -	1,145.31	1,327.00	- -	03/2021	4.10
413	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]	11/2016	290.73 -	315.00	246.70	- -	-	8.35
414	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]	11/2012	605.84 -	722.46	722.46	07/2018 -	-	19.25
415	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG- II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	03/2017	1,184.71 -	1,310.00	1,039.23	03/2020 -	-	10.58
416	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	03/2017	744.64 -	982.00	-	03/2020 -	-	31.88

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
417	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	03/2017	1,030.44 -	1,065.51	1,015.76	03/2020 -	-	3.40
418	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	03/2017	988.34 -	1,043.28	1,035.00	03/2020 -	-	5.56
419	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]	03/2017	1,059.73 -	1,071.00	610.87	03/2017 -	-	1.06
420	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]	03/2017	1,098.06 -	1,160.64	1,068.76	03/2020 -	-	5.70
421	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	03/2017	754.54 -	756.27	379.05	03/2020 -	12/2021	.23
422	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	03/2017	672.89 -	736.01	31.82	03/2020 -	-	9.38
423	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]	03/2017	1,041.62 -	1,187.10	951.13	03/2020 -	-	13.97
424	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]	03/2017	1,288.07 -	1,420.00	842.24	03/2020 -	06/2021	10.24
425	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	03/2017	2,064.99 -	2,447.00	2,357.84	03/2020 -	-	18.50
426	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]	03/2017	831.58 -	1,177.00	912.40	03/2020 -	-	41.54
427	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]	03/2017	993.16 -	1,434.00	1,201.43	03/2020 -	-	44.39
428	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]	04/2017	894.00 -	929.32	810.00	04/2020 -	07/2021	3.95
429	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]	06/2017	1,958.88 -	1,993.81	1,116.85	06/2020 -	02/2021	1.78
430	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]	09/2017	1,124.11 -	1,232.76	527.67	09/2017 -	05/2021	9.67
431	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]	12/2017	404.94 -	448.18	427.22	- -	10/2020	10.68
432	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]	01/2018	273.46 -	276.17	72.53	- -	-	.99
433	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]	02/2018	1,424.77 -	1,853.42	14.19	- -	-	30.09
434	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]	02/2018	1,166.26 -	1,296.93	220.78	- -	08/2021	11.20

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
435	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787	02/2018	1,995.34 -	2,400.00	3,088.59	- -	11/2021	20.28
436	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789	02/2018	2,177.80 -	2,450.00	2,244.98	- -	-	12.50
437	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790	03/2018	1,261.98 -	1,952.20	934.06	- -	07/2021	54.69
438	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793	03/2018	925.40 -	1,197.00	1,011.70	- -	-	29.35
439	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800	03/2018	1,120.57 -	1,332.00	1,118.92	- -	-	18.87
440	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801	02/2018	1,052.21 -	1,449.00	342.39	- -	01/2021	37.71
441	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807	03/2018	1,532.62 -	2,499.00	761.73	03/2021 -	04/2021	63.05
442	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813	03/2018	496.20 -	537.17	38.11	- -	-	8.26
443	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814	03/2018	1,029.96 -	1,261.05	197.88	- -	03/2021	22.44
444	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829	03/2018	1,016.92 -	1,071.00	218.47	- -	01/2022	5.32
445	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830	03/2018	2,065.96 -	2,169.00	-	- -	-	4.99
446	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831	03/2018	1,294.47 -	1,296.00	-	- -	-	.12
447	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839	03/2018	634.70 -	931.21	268.17	- -	07/2021	46.72
448	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841	03/2018	795.50 -	799.30	213.17	- -	07/2021	.48
449	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853	03/2018	642.13 -	807.00	666.56	- -	-	25.68
450	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199	10/2019	743.88 -	743.89	298.54	- -	12/2021	.00

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
451	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212	12/2017	656.98 -	840.00	105.50	- -	11/2022	27.86
452	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214	12/2017	217.96 -	884.00	257.13	- -	-	305.58
	Total		94,703.35 -	1,21,666.27	89,812.01			
	<u>RURAL DEVELOPMENT</u>							
	<u>Hindustan Steelwork Construction Limited</u>							
453	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099	12/2007	202.61 227.00	207.12	190.22	12/2016 -	10/2021	2.23
454	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098	03/2007	149.73 173.00	155.66	144.95	12/2015 -	10/2021	3.96
	Total		352.34 -	362.78	335.17			
	<u>STEEL</u>							
	<u>National Mineral Development Corporation (Nmhc)</u>							
455	NMDC INTEGRATED STEEL PLANT - [N12000086	01/2010	15,525.00 -	21,940.00	18,516.49	05/2015 -	07/2021	41.32
	Total		15,525.00 -	21,940.00	18,516.49			
	<u>TELECOMMUNICATIONS</u>							
	<u>Department Of Telecommunication</u>							
456	NETWORK FOR SPECTRUM - [N26000101	03/2012	13,334.00 -	24,664.00	17,845.00	07/2015 -	07/2021	84.97
	Total		13,334.00 -	24,664.00	17,845.00			
	<u>URBAN DEVELOPMENT</u>							
	<u>Ahmedabad Metro Rail</u>							
457	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122	11/2014	10,773.00 -	12,787.00	8,768.08	12/2018 -	08/2022	18.69
	<u>Bangalore Metro Rail Corporation Limited</u>							
458	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058	02/2014	26,405.14 -	30,695.12	17,021.86	02/2019 -	06/2024	16.25
	<u>Central Public Works Department</u>							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
459	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]	12/2008	114.26 266.00	266.00	-	12/2013 -	-	132.80
	<u>Chennai Metro Rail Ltd</u>							
460	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]	02/2009	14,600.00 -	19,058.00	16,365.87	12/2015 -	-	30.53
	<u>Kochi Metro Rail Corporation Ltd</u>							
461	KOCHI METRO RAIL PROJECT - [N28000081]	07/2012	5,181.79 -	6,218.14	6,059.17	07/2017 -	-	20.00
	<u>Mumbai Metro Rail Corporation Ltd</u>							
462	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]	07/2013	23,136.00 -	33,406.00	17,039.36	01/2015 -	03/2023	44.39
	<u>National Building Construcion Corporation Ltd</u>							
463	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	06/2012	4,264.00 -	4,720.73	4,683.08	11/2019 -	-	10.71
	Total		84,474.19 -	1,07,150.99	69,937.42			
	<u>WATER RESOURCES</u>							
	<u>Kolkata Metropolitan Development Authority</u>							
464	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]	05/2018	198.43 -	224.69	-	02/2022 -	06/2022	13.23
	<u>Polavaram Project Authority</u>							
465	POLAVARAM IRRIGATION PROJECT - [N30000002]	02/2009	10,151.04 -	55,548.87	17,325.20	03/2020 -	04/2022	447.22
	<u>Uttar Pradesh Jal Nigam</u>							
466	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]	10/2017	213.62 -	261.12	-	03/2022 -	03/2022	22.24
467	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR - [N30000009]	10/2016	370.40 -	430.49	376.22	08/2020 -	-	16.22
468	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020]	02/2011	279.91 -	330.05	244.84	12/2019 -	01/2021	17.91
469	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]	01/2019	231.79 -	234.03	-	12/2021 -	12/2021	.97
470	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]	02/2019	681.78 -	690.71	-	06/2022 -	06/2022	1.31
	Total		12,126.97 -	57,719.96	17,946.26			
	Grand Total		7,74,185.41	12,53,567.06	754,771.67			

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(APRIL 2021)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	03/2023	12320	75
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	02/2022	11459	74
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2022	3492	145
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	NPCIL	03/2013	11/2020	11/2023	39849	36

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
5	DEVELOPMENT OF TUTICORIN AIRPORT	AAI	06/2019	03/2022	03/2023	380.87	12
6	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT	AAI	08/2017	02/2020	12/2021	177.1	22
7	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN	AAI	07/2018	09/2020	12/2021	456.86	15
8	UPGRADATION OF JABALPUR AIRPORT	AAI	06/2016	06/2021	12/2021	412.24	6
9	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	AAI	12/2016	03/2021	03/2022	1142	12
10	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	AAI	01/2016	03/2020	12/2021	458	21
11	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPORT	AAI	11/2016	04/2020	03/2022	303.8	23
12	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2021	417.23	33
13	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	AAI	06/2018	02/2022	08/2022	2467	6
14	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AIRPORT	AAI	08/2018	10/2021	07/2022	951.28	9
15	CCS INTERNATIONAL AIRPORT , LUCKNOW	AAI	06/2018	09/2021	09/2022	1383	12
16	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA	AAI	01/2019	11/2021	10/2022	389.71	11
17	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	AAI	09/2015	06/2019	06/2021	438.28	24

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
18	2.0 MTPA BHOJUDIH NLW WASHERY	BCCL	12/2015	03/2017	03/2022	304.13	60
19	PATHERDIH 2.5 NLW COAL WASHERY	BCCL	10/2015	04/2018	06/2022	243	50
20	PACHWARA SOUTH COAL BLOCK	NLC	07/2013	08/2022	09/2023	1795.01	13

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
21	JALAGAM VENGALA RAO OCP-II	SCCL	07/2011	03/2015	03/2023	447.06	96
22	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2022	162.76	84
23	KALYANIKHANI OPENCAST PROJECT	SCCL	07/2012	07/2016	03/2022	417.33	68
24	RECAST EPR AMRAPALI OC	CCL	02/2012	03/2020	03/2024	4983.58	48
25	AMADAND OPENCAST EXPANSION PROJECT	SECL	03/2016	03/2021	03/2022	869.44	12
26	AMALGAMATED GONDEGAON GHATROHAN OC	WCL	02/2016	03/2019	03/2022	198.68	36
27	BHATADI EXPANSION OC MINE	WCL	02/2016	03/2019	09/2026	304.52	90
28	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	NLC	07/2016	11/2021	07/2022	17237	8
29	RPR FOR JAMUNIA UG (0.90 MTY)	WCL	07/2016	03/2022	03/2026	281.25	48
30	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	NLC	04/2013	06/2015	03/2025	1458.17	117
31	REVISED PR FOR AMALGAMATED INDER KAMPTEE DEEP OC (3.2 MTY)	WCL	11/2015	03/2021	03/2024	313.34	36
32	RPR FOR MUNGOLI NIORGUDA EXTENSION (DEEP) OC (4.375 MTY)	WCL	11/2015	03/2020	03/2026	851.6	72
33	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	ECL	08/2012	03/2018	10/2021	1055.05	43
34	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	MCL	05/2014	03/2019	03/2024	479.15	60
35	GARJANBAHAL OCP	MCL	11/2014	03/2021	03/2024	1375.38	36
36	PR FOR DINESH(MAKARDHOKRA III) EXPANSION OC (8.0 MTY)	WCL	11/2014	03/2020	03/2027	1184.33	84
37	AMERA OC RCE	SECL	02/2015	03/2018	03/2023	335.97	60
38	RAJNAGAR OCP RPR (1.70 MTY)	SECL	12/2014	03/2021	04/2024	357.8	37
39	KANCHAN OC EXPANSION	SECL	12/2014	03/2021	03/2024	371.04	36
40	MADHUBAND NLW WASHERY	BCCL	08/2010	05/2014	07/2021	289.45	86
41	NEW MAJRI UG TO OC	WCL	05/2015	03/2019	09/2026	295.56	90
42	KAKATIYAKHANI OPENCAST-2 PROJECT	SCCL	05/2015	03/2019	03/2022	397.09	36
43	SINGHORI OC MINE	WCL	06/2015	03/2020	09/2021	205.49	18

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
44	ADASA UG TO OC	WCL	08/2015	03/2023	03/2024	288.9	12
45	AMGAON OPENCAST PROJECT RCE	SECL	07/2015	03/2020	03/2023	316.1	36
46	JAYANT EXPANSION OCP 10 TO 20 MTPA	NCL	05/2017	03/2021	03/2022	1783.09	12
47	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2022	152.43	84
48	MAGADH EXPANSION OC(51 MTY)	CCL	08/2008	07/2012	03/2025	6964.33	152
49	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2023	418.97	132
50	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2022	163.51	132
51	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2022	162.46	96
52	EXPANSION PR OF JHANJRA UG(5.00 MTY)	ECL	11/2015	03/2022	03/2029	1210.12	84
53	KISTARAM OCP	SCCL	11/2010	03/2015	03/2022	242.29	84
54	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2022	178.44	96
55	DURGAPUR OPENCAST PROJECT	SECL	02/2015	03/2023	03/2026	916.24	36
56	RAJRAPPA RCE OCP (3.0 MTY)	CCL	12/2009	03/2016	03/2022	510.85	72
57	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY)	MCL	12/2007	03/2013	03/2028	8416.19	180
58	BHUBANESWARI EXPENSION OCP(40.0 MTY)	MCL	12/2007	03/2017	03/2031	3145.45	168
59	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2022	479.53	108
60	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY)	MCL	12/2007	03/2010	03/2029	3504.21	228
61	MURAIIDH UG TURN-KEY PROJECT	BCCL	02/2011	04/2014	04/2023	339.88	108
62	MOONIDIH XV SEAM UG	BCCL	08/2011	04/2015	03/2022	1230.27	83
63	RECAST PR FOR DHANKASA UG (1.00 MTY)	WCL	09/2016	03/2022	03/2025	289.29	36
64	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY)	WCL	02/2017	03/2021	09/2023	328	30
65	KOLAR PIMPRI EXTENSION OC	WCL	03/2017	03/2020	09/2022	362.73	30
66	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1	SCCL	03/2017	03/2019	03/2022	413.84	36

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
67	DUDHICHA EXPANSION OCP (10 TO 20 MTPA)	NCL	11/2017	03/2022	03/2023	1255.17	12
68	BELLORA-NAIGAON DEEP OC	WCL	11/2018	03/2021	09/2022	252.71	18
69	UKNI DEEP OC	WCL	11/2018	03/2021	09/2022	318.14	18

DEFENCE PRODUCTION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
70	RESIDENTIAL QUATERS FOR HAL, BANGLORE	CPWD	12/2016	02/2020	12/2021	246.31	22

DPIIT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
71	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	IICC	11/2017	12/2019	12/2021	4773	24
72	DELHI MUMBAI INDUSTRIAL CORRIDOR	DMIC	09/2011	09/2019	07/2021	12579.09	22

FERTILISERS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
73	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY	RCF	04/2018	04/2020	07/2021	426.72	15
74	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL	NFL	01/2018	11/2019	04/2021	239.81	17
75	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT	NFL	01/2018	11/2019	05/2021	215.92	18
76	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA	NFL	01/2018	11/2019	04/2021	218.83	17

FINANCE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
77	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	CPWD	12/2015	10/2019	07/2021	209	21

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
78	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT	CPWD	03/2018	09/2020	04/2022	195	19
79	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST)	CPWD	09/2017	03/2020	12/2021	150.29	21
80	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	HSCC	08/2017	03/2019	06/2021	355.15	27

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
81	LHMC NEW DELHI-RE-DEVELOPMENT	HSCC	02/2013	11/2013	05/2021	414.11	90
82	NEIGRIHMS SHILLONG MEGHALYA	HSCC	10/2016	05/2018	12/2021	363.99	43
83	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD	CPWD	10/2016	03/2020	05/2021	209.84	14
84	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH	CPWD	12/2018	06/2021	05/2022	260	11
85	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	HITES	05/2017	05/2021	07/2022	875	14
86	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	HITES	07/2016	06/2020	07/2021	703	13
87	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	HITES	07/2016	04/2020	07/2021	785	15

HOME AFFAIRS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
88	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	12/2021	1219.21	26
89	NSG AT KOLKATA	CPWD	10/2014	04/2018	12/2021	162.88	44

HUMAN RESOURCE DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
90	PERMANENT CAMPUS FOR IIM BODH GAYA	CPWD	09/2018	09/2020	11/2022	375	26
91	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE 1A AT PUDESSERY VILLAGE, KANJIKODE WEST, DISTRICT PALAKKA	CPWD	07/2019	03/2021	06/2022	753.63	15
92	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A)	CPWD	07/2019	03/2022	09/2022	851	6
93	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	CPWD	02/2016	06/2017	10/2021	496.18	52
94	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	CPWD	01/2018	05/2020	02/2022	430	21
95	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR	CPWD	11/2017	03/2020	06/2021	171.72	15
96	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	CPWD	09/2012	03/2016	06/2021	171.86	63
97	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	CPWD	08/2016	04/2019	05/2021	294	25
98	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI	CPWD	01/2018	07/2020	06/2021	223.37	11

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(APRIL 2021)

MINES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
99	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	NALCO	12/2014	04/2021	12/2022	5540	20
100	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN	NALCO	11/2017	04/2021	03/2023	483	23

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
101	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT	GAIL	08/2018	04/2021	10/2021	217.92	6
102	LPG BP PROJECT MOTIHARI	IOCL	05/2018	03/2021	09/2021	206.5	6
103	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	IOCL	04/2018	02/2020	08/2021	206.63	18
104	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY	IOCL	08/2017	08/2020	11/2021	255.4	15
105	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY	IOCL	12/2017	10/2020	08/2022	199.36	22
106	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE	IOCL	10/2017	02/2020	10/2021	906	20
107	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	OIL	01/2018	02/2020	06/2021	543.91	16
108	BS VI PROJECT AT GUWAHATI REFINERY	IOCL	08/2018	02/2020	06/2021	557	16
109	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT	IOCL	08/2018	08/2020	04/2022	1636	20
110	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY	IOCL	01/2019	01/2021	03/2022	909	14
111	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY	IOCL	10/2018	02/2020	02/2022	598	24
112	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT	GAIL	08/2018	08/2020	06/2021	286.42	10
113	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN	OIL	06/2016	08/2020	06/2021	224.75	10
114	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION	ONGC	02/2019	05/2021	12/2021	2292.46	7
115	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	ONGC	04/2019	03/2022	05/2023	3228.8	14
116	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV	ONGC	05/2019	05/2021	01/2022	3660.71	8
117	ADDITIONAL STORAGE TANKS AT PARADIP	IOCL	11/2018	09/2021	06/2022	462.3	9
118	Fuel Quality Upgradation Project at Paradip Refinery	IOCL	05/2019	08/2021	09/2022	3361	13
119	ENNORE THIRUVALUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	02/2022	4497	38

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
120	BSVI UPGRADATION	MANGALORE REFI	09/2016	12/2019	02/2022	1810	26
121	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I)	OIL	05/2016	10/2020	03/2022	406	17
122	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II	OIL	09/2016	12/2019	08/2021	571.66	20
123	MMPL PIPELINE REROUTING PROJECT	BPCL	04/2013	12/2019	04/2021	449.58	16
124	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY	BPCL	02/2016	02/2020	05/2021	3313	15
125	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	IOCL	05/2016	01/2021	09/2021	212	8
126	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	IOCL	05/2016	01/2021	10/2021	348	9
127	DURGAPUR-HALDIA PIPELINE PROJECT	GAIL	03/2017	12/2020	12/2021	1740	12
128	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	05/2021	4588.29	33
129	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	GAIL	04/2016	04/2018	06/2021	327.78	38
130	IRUGUR-DEVANGONTHI POL PIPELINE	BPCL	11/2012	02/2017	08/2022	678	66
131	VISAKH REFINERY MODERNISATION PROJECT	HPCL	07/2016	07/2020	07/2022	20928	24
132	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	IOCL	06/2016	08/2019	06/2021	423	22
133	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	ONGC	11/2015	03/2019	09/2021	650.82	30
134	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	ONGC	03/2016	06/2020	06/2022	34012	24
135	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	IOCL	05/2016	01/2021	09/2021	261	8
136	PIPELINE NETWORK PROJECT GELEKI, ASSAM	ONGC	07/2016	05/2020	05/2021	249.85	12
137	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	HPCL	09/2017	06/2021	08/2022	2677	14
138	KHARAGPUR LPG BOTTLING PLANT	IOCL	04/2017	04/2020	10/2021	163.02	18
139	RE-LIQUIFIED NATURAL GAS	CPCL	08/2017	08/2020	09/2021	421	13
140	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS, HSD AND	IOCL	08/2017	06/2020	09/2021	236	15
141	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	IOCL	12/2017	10/2020	01/2022	466.43	15
142	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA	HPCL	11/2017	11/2020	06/2021	255	7

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
143	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	05/2022	3190.69	49
144	SITARGANJ LPG PROJECT	IOCL	02/2017	02/2020	06/2021	160.1	16
145	LPG BP PROJECT KHORDHA	IOCL	12/2016	12/2019	03/2022	161.59	27
146	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	02/2022	2915	110
147	SEA WATER DESALINATION PLANT	MANGALORE REFI	11/2017	03/2020	07/2021	581	16
148	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	03/2022	607.06	53
149	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	IOCL	01/2015	03/2021	12/2021	1823	9
150	PARADIP HYDERABAD PIPELINE	IOCL	01/2015	12/2020	03/2022	2321	15
151	PARADIP LPG IMPORT FACILITY	IOCL	01/2015	07/2018	05/2021	690	34
152	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	02/2022	861.79	105
153	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT	GAIL	07/2015	12/2020	09/2021	2881.4	9
154	DHAMRA-ANGUL PIPELINE PROJECT	GAIL	03/2017	12/2020	12/2021	1933	12
155	DOBHI-DURGAPUR PIPELINE PROJECT	GAIL	03/2017	12/2020	06/2021	2433	6
156	BOKARO-ANGUL PIPELINE PROJECT	GAIL	03/2017	12/2020	12/2021	3437	12
157	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	02/2022	1112	32
158	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA	HPCL	06/2017	06/2020	09/2021	249.26	15
159	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE	HPCL	06/2017	06/2020	09/2021	161.5	15
160	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH	IOCL	08/2018	04/2021	12/2021	466	8
161	REVAMPING OF FACILITIES AT VIZAG TERMINAL	IOCL	04/2018	04/2022	02/2023	355	10
162	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR	IOCL	04/2018	03/2021	12/2021	522	9
163	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI	GAIL	09/2018	02/2021	12/2021	225.54	10
164	GRASS ROOT TERMINAL AT MALKAPUR	IOCL	12/2018	04/2022	08/2023	611	16
165	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT	IOCL	12/2018	06/2021	07/2022	278.6	13

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	220 KV, PANIPAT						
166	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT	BPCL	07/2017	02/2021	03/2023	580.2	25
167	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY	IOCL	06/2019	09/2022	03/2023	371	6
168	R and D CAMPUS II AT FARIDABAD	IOCL	06/2019	12/2022	07/2023	2281.94	7
169	SWRO II WITH LLPH FACILITIES	HPCL	09/2019	07/2020	07/2021	196.26	12
170	COMPRESSED BIO GAS PLANT AT GORAKHPUR	IOCL	09/2019	07/2021	03/2022	164.69	8

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
171	DURGAPUR PP-III (2X20 MW) - NSPCL	NTPC	12/2016	11/2018	07/2021	529.68	32
172	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL	NTPC	05/2016	12/2018	07/2021	1885.13	31
173	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	12/2018	05/2021	12532.44	29
174	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	10/2022	14366.58	40
175	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	12/2024	1381.84	63
176	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	PGCIL	03/2015	03/2018	06/2021	197.4	39
177	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	PGCIL	03/2015	05/2017	09/2021	1394.52	52
178	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	07/2012	07/2021	5353	108
179	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2023	2491.58	126
180	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	07/2023	8692.97	141
181	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P	PGCIL	05/2016	11/2019	06/2021	14733.37	19
182	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/	PGCIL	02/2017	02/2019	09/2021	322.3	31
183	EASTERN REGION STRENGTHENING SCHEME XVII(PART B)	PGCIL	02/2017	06/2019	06/2021	235.53	24
184	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII	PGCIL	03/2017	12/2019	09/2021	379.95	21
185	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR	PGCIL	02/2017	04/2020	06/2021	5070.13	14
186	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND	PGCIL	12/2014	12/2018	03/2024	4754.42	63

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	DISTRIBUTION SYSTEM IN A P						
187	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	12/2021	5111.33	36
188	EASTERN REGION STRENGTHENING SCHEME XX	PGCIL	11/2017	05/2020	05/2021	358.83	12
189	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	CPWD	10/2017	11/2019	06/2021	271.9	19
190	AMELIA COAL MINE	THDCIL	01/2017	09/2020	08/2022	2104.21	23
191	EASTERN REGION STRENGTHENING SCHEME-XVIII	PGCIL	03/2017	07/2020	06/2021	3500	11
192	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY	PGCIL	05/2017	07/2019	06/2021	186.17	23
193	HVDC BIPOLE LINK BETWEEN WR AND SR - NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN	PGCIL	08/2017	02/2020	06/2021	1931.39	16
194	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	12/2021	12964.6	43
195	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	07/2022	3919.59	154
196	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	08/2023	6285.33	155
197	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	08/2022	11130.19	108
198	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	PGCIL	01/2014	04/2016	06/2021	374.63	62
199	EASTERN REGION STRENGTHENING SCHEME-XII	PGCIL	05/2014	11/2016	06/2021	522.29	55
200	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2022	2978.48	117
201	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	CVPPPL	10/2014	04/2020	07/2025	8112.12	63
202	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	NTPC	01/2016	11/2020	07/2022	10598.98	20
203	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	PGCIL	03/2016	01/2018	05/2021	808.63	40
204	EASTERN REGION STRENGTHENING SCHEME-XV	PGCIL	04/2016	04/2018	05/2021	454.11	37
205	KHURJA SUPER THERMAL POWER PROJECT	THDCIL	03/2019	09/2023	08/2024	11089.42	11
206	PATRATU STPP-I (3X800MW)	NTPC	11/2017	03/2023	09/2024	18668	18

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
207	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI	NR	06/2009	08/2016	08/2025	404	108

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
208	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW	BITES	02/2016	03/2020	06/2021	393.98	15
209	INDORE-DEWAS-UJJAIN (80 KMS)	WR	04/2016	06/2020	03/2023	700	33
210	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	IRCON	04/2013	09/2018	03/2022	3055	42
211	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	WR	02/1991	03/2019	10/2021	551.51	31
212	ANUPPUR-KATNI	SECR	04/2015	12/2021	12/2023	1370	24
213	BONDAMUNDA RANCHI DOUBLING	SER	03/2016	03/2021	12/2023	1724.2	33
214	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	RVNL	04/2015	03/2022	12/2024	943.6	33
215	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	03/2030	1027.4	324
216	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	06/2022	927.01	39
217	MAU-GHAZIPUR-TARIGHAT NEW LINE	RVNL	04/2015	03/2023	12/2024	1765.92	21
218	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	12/2021	713.48	21
219	VIZIANAGARAM -SAMABALPUR 3RD LINE	RVNL	01/1991	12/2024	12/2026	2335.67	24
220	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	12/2021	948.04	21
221	RAIPUR - TITLAGARH - DOUBLING	RVNL	03/2007	03/2020	12/2021	1402.02	21
222	KIUL - GAYA DOUBLING PROJECT	ECR	12/2015	03/2020	03/2023	1200.2	36
223	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	ECR	12/2015	03/2020	03/2023	1491.47	36
224	KATNI - SINGRAULI DOUBLING PROJECT	WCR	12/2015	03/2020	03/2024	1763.93	48
225	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	CR	02/2015	03/2022	03/2023	1272.19	12
226	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	CR	02/2015	03/2023	03/2024	2449.91	12
227	MANMAD - JALGAON - 3RD LINE (160 KM)	CR	02/2016	03/2022	03/2024	1035.16	24
228	WARDHA - NAGPUR - 4TH LINE (76 KM)	CR	02/2016	03/2023	03/2024	637.95	12
229	GUNTUR-GUNTAKAL	SCR	04/2016	03/2022	03/2024	3631	24
230	JAGADALPUR-KORAPUT DOUBLING	ECOR	04/2015	03/2022	03/2023	1547.38	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
231	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	09/1995	03/2020	03/2025	303.98	60
232	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	WR	04/2008	03/2012	03/2023	318.24	132
233	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	03/2024	829.74	48
234	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	03/2022	1503.71	24
235	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	12/2021	1111.99	34
236	BHADRAK - NERGUNDI 3RD LINE	ECOR	03/2013	10/2020	03/2024	843.04	41
237	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	03/2020	03/2023	1160	36
238	SAMBALPUR - ANGUL RLY. ELECTRIFICATION	ECOR	03/2012	03/2020	03/2022	155.81	24
239	CHOTTAUDEPUR-DHAR(NL)	WR	04/2007	03/2022	03/2023	1347.26	12
240	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2024	1045.2	180
241	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	03/2025	1188.91	72
242	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	03/2024	607.09	133
243	RAMGANJMUNDI-BHOPAL (NL),WCR	WCR	04/2001	03/2021	03/2023	424.6	24
244	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	06/2022	1202.7	88
245	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	03/2025	810.78	45
246	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	SR	09/2007	02/2019	03/2025	724.69	73
247	BARDHAMAN-KATWA (GC)	ER	04/2007	12/2010	03/2025	1106.62	171
248	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	03/2023	2393.47	108
249	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	07/2021	477.88	112
250	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	03/2010	03/2024	1160.48	168
251	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	03/2025	2913.51	108
252	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	03/2024	3503.69	24
253	SONDALIA-CHAMPAPUKUR DOUBLING WITH	ER	04/2010	03/2016	03/2025	277.28	108

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	NEW MM FOR BIRA-CHAKIA NL						
254	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL	ER	04/2010	03/2017	03/2025	365.17	96
255	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	03/2023	792.89	24
256	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY	ER	04/2011	03/2017	03/2026	299.6	108
257	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI- ULUBERIA(BIRSHIVPUR) AND PUJALI- BAHRAHAT NL	ER	04/2010	03/2005	03/2025	494.54	240
258	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	02/2012	03/2025	499.96	157
259	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL	ER	04/2009	03/2014	03/2025	257.42	132
260	WARDHA-SEWAGRAM NGP 3RD LINE	CR	04/2012	03/2022	03/2024	540.02	24
261	BAGALKOT-KUDACHI NL	SWR	04/2010	03/2016	12/2023	986.3	93
262	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	03/2023	03/2024	1856.95	12
263	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	06/2021	287	114
264	SHIMOGA-HARIHAR NL	SWR	04/2011	03/2016	03/2024	832.47	96
265	NADIKUDE-SRI KALAHASTI	SCR	04/2011	03/2021	03/2024	2288.7	36
266	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	03/2020	06/2021	704.31	15
267	KADAPA-BANGALORE (NL), KADAPA- PENDLIMARRI PH-I	SCR	04/2008	03/2014	03/2027	2132.77	156
268	GADAG-WADI NL	SWR	04/2013	12/2018	06/2025	2841.84	78
269	MARIKUPPAM - KUPPAM	SWR	04/2012	03/2016	12/2023	279.54	93
270	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	03/2023	2271.5	24
271	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	03/2022	495.44	216
272	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2025	247.66	202
273	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	11/2022	324.73	128
274	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	05/2021	1180.19	149
275	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	03/2026	2923.13	204

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
276	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	12/2023	4454.17	153
277	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	12/2021	495.74	102
278	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	03/2023	385.2	48
279	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	03/2024	532.87	60
280	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	12/2024	2326.52	117
281	DAUSA-GANGAPUR CITY(NL),NWR	NWR	02/1997	02/2019	06/2022	410.08	40
282	NANGALDAM-TALWARA(NL),NR	NR	03/1981	07/2012	03/2024	450	140
283	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	NR	03/1995	11/2002	12/2022	2500	241
284	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	03/2025	3951.98	108
285	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	141
286	MUNEERABAD-MAHABOBNAGAR(NL),SCR	SCR	04/1997	03/2000	03/2023	1723	276
287	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	04/2020	04/2021	511.86	12
288	BANGLORE - SATYAMANGALAM (NL)(SWR)	SWR	04/1996	03/2002	03/2024	1382.78	264
289	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	WR	04/2007	03/2022	03/2023	1640.04	12
290	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	03/2023	320.66	48
291	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	03/2021	12/2021	1037.15	9
292	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	12/2024	2912.96	33
293	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR	NWR	04/2013	03/2020	06/2021	420.18	15
294	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	03/2025	651	120
295	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	12/2018	04/2021	258.2	28
296	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	03/2023	548	36
297	HUBLI- CHIKJAJUR	SWR	03/2015	03/2020	03/2023	1156.94	36
298	PHULERA - DIGANA DOUBLING	NWR	05/2015	03/2020	10/2022	600	31

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
299	YELAHANKA-PENUKONDA	SWR	05/2015	03/2020	06/2021	860.43	15
300	ARSIKERE-TUMKUR	SWR	03/2015	03/2020	06/2021	578	15
301	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	03/2024	1614.59	60
302	HAJIPUR - BACHAWARA	ECR	05/2015	03/2019	05/2021	678.54	26
303	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	02/2022	295	37
304	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	M RTP	03/2013	03/2016	06/2021	4874.58	63
305	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	NFR	04/2013	03/2019	03/2024	1798	60
306	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	03/2022	569.63	24
307	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2021	632.68	69
308	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	03/2019	12/2027	120.7	105
309	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	ER	04/1987	03/2006	03/2025	406.99	228
310	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	03/2025	915.98	36
311	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3	ER	04/2001	03/2016	03/2025	923.52	108
312	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	ER	04/2005	03/2017	03/2025	595.51	96
313	KOTTAVALSA - KORAPUT DOUBLING	ECOR	04/2015	03/2022	03/2024	2499.71	24
314	KORAPUT - SINGAPUR ROAD DOUBLING	ECOR	04/2015	03/2022	03/2026	2361.74	48
315	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	03/2024	701.61	64
316	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	ECOR	04/2015	12/2018	03/2024	1172.92	63
317	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	NFR	04/2015	03/2022	03/2023	2232.32	12
318	SURENDRA NAGAR RAJKOT	WR	04/2015	03/2021	12/2022	1002.39	21
319	KAZIPET-BALHRSHA	SCR	04/2015	03/2021	03/2024	2063.03	36
320	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	12/2021	969.83	21
321	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	06/2022	942.95	39

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
322	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	RVNL	03/2012	12/2020	12/2022	1183.25	24
323	BINA - KOTA DOUBLING WITH RE	RVNL	04/2011	12/2020	12/2021	1485.85	12
324	KATNI-BINA 3RD LINE (263 KM)	WCR	06/2016	03/2022	03/2023	2478.23	12
325	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	03/2023	582.13	12
326	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	SCR	04/2017	03/2022	12/2022	119.73	9
327	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	12/2021	585.93	34
328	NANPARA - NEPALGANJ GAUGE CONVERSION.	NER	04/2017	04/2017	10/2022	150	66
329	ETAH - KASGANJ - NEW LINE	NER	04/2017	04/2017	04/2022	276.9	60
330	GARHWA ROAD-RAMNA	ECR	03/2015	03/2021	03/2022	348.23	12
331	CHANDIGARH-BADDI	NR	04/2007	03/2023	03/2025	328.14	24
332	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING.	NER	04/2016	12/2019	04/2021	1177.96	16
333	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	03/2024	744.04	36
334	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM	ECR	04/2016	03/2021	06/2022	731.64	15
335	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	12/2024	229	36
336	JHARSUGUDA-BILASPUR 4TH LINE	SECR	04/2015	03/2021	12/2023	1973	33
337	RAMNA - SINGRAULI DOUBLING	ECR	08/2015	03/2020	03/2024	2436.21	48
338	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL	IRCON	04/2016	03/2020	03/2024	5200	48
339	KARAILA ROAD - SHAKTINAGAR DOUBLING	ECR	08/2015	03/2019	03/2022	528.57	36
340	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	12/2023	1908.51	9
341	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	SR	02/1996	03/2005	09/2021	268.87	198
342	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM)	SR	02/2017	03/2024	03/2026	1567	24
343	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	SR	02/2015	03/2020	06/2022	760	27
344	INDARA - DOHRIGHAT GAUGE CONVERSION.	NER	04/2016	04/2016	12/2021	213	68

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
345	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI.	NER	04/2016	01/2022	03/2025	1900	38
346	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	03/2025	644.78	96
347	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	12/2023	2288	21
348	JALANDHAR-PATHANKOT-JAMMU TAWI	NR	03/2002	03/2016	06/2021	625	63

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
349	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K	MORTH	08/2020	11/2020	08/2022	196.23	21
350	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO	NHAI	02/2019	03/2020	04/2022	847	25
351	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 KM	MORTH	11/2018	12/2020	06/2021	281.45	6
352	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE	NHAI	02/2019	12/2019	12/2021	990.97	24
353	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS- CONTROLLED EXPRESSWAY FROM BAWDI VILLAG	NHAI	03/2019	05/2020	05/2022	1047	24
354	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MORTH	08/2010	10/2010	06/2021	193.69	128
355	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM.	MORTH	04/2013	08/2013	06/2021	166.27	94
356	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	MORTH	01/2013	02/2013	06/2021	182.28	100
357	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	MORTH	08/2010	10/2010	06/2021	195.04	128
358	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	NHAI	08/2017	08/2017	02/2022	950.64	54
359	FOUR LANNING OF CHOLOPURAM-THANJAVUR	NHAI	08/2017	08/2017	07/2022	1176.37	59
360	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	NHAI	07/2017	07/2017	06/2021	476.56	47
361	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	05/2021	1124.11	44
362	4-LANNING OF STHIYATHOPU-CHOLOPURAM	NHAI	09/2017	09/2017	07/2022	1227.87	58
363	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	NHIDCL	06/2015	06/2018	12/2021	437.39	42
364	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5	NHIDCL	06/2015	06/2018	12/2021	463.49	42
365	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO	MORTH	11/2013	05/2017	04/2021	497.05	47

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	65/870						
366	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400	MoRTH	11/2015	01/2020	06/2021	628.45	17
367	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93	MoRTH	12/2015	02/2020	04/2021	957.54	14
368	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200	MoRTH	03/2015	08/2017	06/2021	511.83	46
369	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) 0	NHIDCL	01/2016	01/2016	04/2021	294.17	63
370	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	MoRTH	11/2011	09/2015	10/2021	954.43	73
371	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS	NHAI	05/2010	05/2013	08/2021	374	99
372	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM)	NHAI	04/2012	04/2014	01/2022	624	93
373	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	12/2022	2848	105
374	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	08/2013	05/2021	1078.84	93
375	4-LANING OF BRAHAMPORE-FARAKA	NHAI	02/2011	08/2013	06/2022	998.79	106
376	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	06/2021	1928.22	74
377	8 LANING OF MUKARBA CHOWK TO PANIPAT	NHAI	07/2015	04/2019	09/2021	2128.72	29
378	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	MoRTH	04/2013	08/2013	06/2021	151.59	94
379	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	06/2021	531.13	37
380	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	NHAI	10/2015	05/2018	06/2021	593.26	37
381	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	NHAI	12/2015	03/2019	03/2022	649.5	36
382	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3	NHAI	08/2015	05/2018	06/2021	505	37
383	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	NHAI	03/2016	03/2019	03/2022	701.4	36
384	NAGPUR RING ROAD PACKAGE-1	NHAI	03/2016	07/2019	12/2021	546	29
385	NAGPUR RING ROAD PACKAGE-2	NHAI	03/2016	07/2019	12/2021	591.66	29
386	HOSPET-BELLARY-KARNATAKA AP BORDER	NHAI	08/2016	03/2019	12/2021	1167.42	33
387	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65.	NHAI	03/2017	03/2020	12/2021	848.45	21

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
388	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN	NHAI	03/2017	03/2020	12/2021	754.54	21
389	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL	NHAI	03/2017	03/2020	05/2021	639.79	14
390	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE	NHAI	03/2017	03/2020	05/2021	235.48	14
391	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	06/2021	1288.07	15
392	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	NHIDCL	01/2017	03/2017	03/2022	1253.1	60
393	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	NHIDCL	03/2016	08/2016	05/2021	373.07	57
394	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	NHIDCL	03/2016	08/2016	05/2021	396.52	57
395	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	NHIDCL	03/2016	08/2016	05/2021	429.52	57
396	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV	NHAI	04/2017	04/2020	07/2021	894	15
397	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P	NHAI	06/2017	06/2020	09/2021	2485.93	15
398	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	NHIDCL	03/2018	09/2018	05/2022	239.3	44
399	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	NHIDCL	03/2018	09/2018	09/2022	285.68	48
400	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	NHIDCL	03/2018	09/2018	12/2021	315.03	39
401	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	NHIDCL	03/2018	09/2018	12/2021	240.64	39
402	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	NHIDCL	03/2018	09/2018	11/2021	215.12	38
403	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	NHIDCL	03/2018	09/2018	12/2021	215.79	39
404	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	NHIDCL	03/2018	09/2018	10/2022	272.89	49
405	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	NHIDCL	03/2018	09/2018	11/2022	323.98	50
406	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A	MORTH	01/2017	09/2019	06/2021	373.82	21
407	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	NHIDCL	03/2018	09/2018	11/2022	500.09	50
408	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	NHIDCL	03/2018	09/2018	07/2022	339.57	46
409	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS	MORTH	01/2016	07/2018	05/2021	809.16	34
410	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM	MORTH	03/2016	06/2019	04/2021	877.79	22

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
411	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH	MoRTH	03/2018	07/2020	08/2021	322.48	13
412	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200	MoRTH	10/2017	10/2019	08/2021	1069.59	22
413	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000	MoRTH	03/2018	11/2020	05/2021	170.57	6
414	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU	MoRTH	09/2016	02/2017	06/2021	372.68	52
415	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69	MoRTH	11/2016	05/2017	07/2021	290.15	50
416	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V	MoRTH	02/2017	11/2017	04/2021	429.43	41
417	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	04/2024	404.29	55
418	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	09/2023	428.11	48
419	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	NHIDCL	08/2017	10/2018	10/2021	517.57	36
420	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS	MoRTH	03/2018	03/2018	06/2021	162.56	39
421	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA	MoRTH	02/2018	03/2018	06/2021	169.63	39
422	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN	MoRTH	01/2017	09/2019	05/2021	396.86	20
423	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19.	MoRTH	02/2018	09/2020	12/2021	426.18	15
424	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS	MoRTH	11/2017	02/2018	06/2021	184.62	40
425	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND	MoRTH	03/2016	08/2019	11/2022	160.27	39
426	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	04/2023	519.09	43
427	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	07/2023	640.07	46
428	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	06/2023	642.96	45
429	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	04/2023	473.18	43
430	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	04/2023	537.82	43
431	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	06/2023	518.53	45
432	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N	MoRTH	06/2016	08/2019	12/2021	236.78	28
433	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF	MoRTH	01/2017	03/2017	06/2021	205.05	51

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	MADHYA PRADESH.						
434	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS	MoRTH	03/2018	03/2018	09/2021	214.69	42
435	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS	MoRTH	03/2018	08/2018	09/2021	217.22	37
436	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS	MoRTH	03/2018	03/2018	06/2021	233.04	39
437	2L+PS OF THIKRI ANJAD SECTION OF NH-347B	MoRTH	11/2017	07/2018	04/2021	249.05	33
438	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS	MoRTH	11/2017	02/2018	06/2021	254.17	40
439	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS	MoRTH	02/2018	03/2018	06/2021	279.44	39
440	REHABILITATION AND UPGRADATION OF KARNATAKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O	MoRTH	03/2016	05/2016	04/2021	995.09	59
441	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM-	MoRTH	02/2018	06/2018	04/2021	370.3	34
442	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM-	MoRTH	02/2018	05/2018	06/2021	341.79	37
443	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P	MoRTH	01/2018	08/2018	05/2021	418.03	33
444	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT	MoRTH	01/2016	08/2016	07/2021	348.95	59
445	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216	MoRTH	01/2017	09/2017	05/2021	263.45	44
446	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA	MoRTH	03/2016	12/2019	06/2021	536.65	18
447	BARASGAON TO RAHATEE	MoRTH	07/2016	09/2018	04/2021	289.11	31
448	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH	MoRTH	10/2013	03/2017	04/2021	445.89	49
449	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM.	MoRTH	11/2017	03/2018	06/2021	392.33	39
450	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION	MoRTH	02/2017	05/2019	05/2021	157.32	24
451	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C	MoRTH	10/2016	08/2020	07/2021	171.9	11
452	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MoRTH	08/2010	09/2014	06/2021	186.96	81
453	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD	MoRTH	01/2019	03/2021	11/2021	264.5	8
454	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750	MoRTH	03/2018	04/2020	04/2021	263.89	12
455	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L	MoRTH	03/2016	09/2020	05/2021	296.5	8

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	WITH PS						
456	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180	MoRTH	01/2016	08/2016	06/2021	497.14	58
457	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION	MoRTH	11/2015	06/2017	06/2021	335.32	48
458	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V	MoRTH	01/2016	09/2016	06/2021	476.2	57
459	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	MoRTH	01/2016	10/2016	06/2021	624.98	56
460	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI	MoRTH	03/2016	07/2016	06/2021	452.94	59
461	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION	MoRTH	12/2014	03/2015	06/2021	496.02	75
462	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A	MoRTH	11/2017	05/2019	06/2021	188.8	25
463	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331	MoRTH	12/2014	11/2017	06/2021	379.16	43
464	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGOUR SECTION BY EXECUTING BALANCE WORK FRO	MoRTH	03/2020	08/2020	08/2022	255.23	24

RURAL DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
465	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	HSCL	03/2007	12/2015	10/2021	149.73	70
466	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	HSCL	10/2011	12/2016	12/2021	175.49	60
467	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	HSCL	12/2007	12/2016	10/2021	202.61	58

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
468	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E	SAIL	12/2018	09/2020	09/2021	263.36	12
469	COKE OVEN BATTERY-5	RINL	12/2011	12/2017	12/2021	2858	48
470	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	SAIL	11/2016	06/2019	08/2021	262.87	26
471	NEW SINTER PLANT AT BOKARO STEEL PLANT	SAIL	03/2015	10/2017	12/2021	1034.01	50
472	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	07/2021	15525	74
473	FORGED WHEEL PLANT	RINL	04/2014	09/2018	06/2021	1682.85	33

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(APRIL 2021)

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
474	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	CPWD	10/2016	03/2018	06/2021	248.2	39
475	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	07/2021	13334	72

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
476	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND	DMRC	05/2017	12/2020	09/2021	565	9
477	AHMEDABAD METRO RAIL PROJECT PHASE 1	MEGA	11/2014	12/2018	08/2022	10773	44
478	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N	CPWD	10/2016	08/2020	03/2022	392	19
479	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I	CPWD	10/2016	07/2021	12/2024	1180	41
480	BANGALORE METRO RAIL PROJECT PHASE-2	BMRC	02/2014	02/2019	06/2024	26405.14	64
481	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	CPWD	06/2015	04/2019	12/2021	197.33	32
482	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	01/2015	03/2023	23136	98
483	DELHI MRTS PHASE-III	DMRC	09/2011	03/2016	09/2021	38585	66

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
484	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR	KMDA	02/2014	12/2019	05/2021	274.76	17
485	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH	KMDA	05/2018	02/2022	10/2022	160	8
486	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	04/2022	10151.04	25
487	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA	BPB	03/2017	12/2019	12/2021	233.57	24
488	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR	BUIDCO	04/2015	04/2020	06/2021	184.93	14
489	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH	UPJalNigam	03/2019	07/2021	06/2022	298.12	11
490	REHABILITATION AND UPGRADE OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S	DJB	05/2016	02/2022	12/2022	239.11	10
491	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2	DJB	05/2016	12/2021	12/2022	211.79	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(APRIL 2021)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	6840	3348
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	11459	16580	5121
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12320	17079	4759

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	417.23	707.73	290.5
5	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	AAI	07/2018	09/2021	346.27	480.33	134.06

COAL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
6	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	152.43	459.49	307.06
7	NEW MAJRI UG TO OC	WCL	05/2015	03/2019	295.56	496.38	200.82
8	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	162.76	349.28	186.52
9	BHATADI EXPANSION OC MINE	WCL	02/2016	03/2019	304.52	729.86	425.34
10	RANIGANJ MASTER PLAN	ECL	08/2009	08/2019	2661.73	5146.48	2484.75
11	AMALGAMATED GONDEGAON GHATROHAN OC	WCL	02/2016	03/2019	198.68	325.18	126.5
12	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	5907.11	7980.79	2073.68
13	BHANEAGAON OC	WCL	02/2015	03/2023	187.94	409.68	221.74

DPIIT

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
14	DELHI MUMBAI INDUSTRIAL CORRIDOR	DMIC	09/2011	09/2019	12579.09	13812.3	1233.21
15	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	IICC	11/2017	12/2019	4773	5178	405

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
16	AIIMS BILASPUR	NBCC	04/2018	09/2021	1351	1471	120
17	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR	CPWD	03/2019	09/2025	1577	1828	251

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
HOME AFFAIRS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
18	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	1219.21	2000	780.79
HUMAN RESOURCE DEVELOPMENT							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
19	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	RITES	09/2013	09/2014	484.32	626.26	141.94
PETROLEUM							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
20	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	OIL	07/2011	03/2017	352.56	490.24	137.68
21	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	607.06	1236	628.94
22	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	861.79	2001	1139.21
23	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	HPCL	09/2017	06/2021	2677	3072	395
24	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	2915	5909	2994
25	MUMBAI REFINERY EXPANSION PROJECT	HPCL	09/2015	03/2020	4199	5060	861
26	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	4497	6025	1528
27	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	ONGC	12/2015	03/2023	823.27	1137.79	314.52
28	VISAKH REFINERY MODERNISATION PROJECT	HPCL	07/2016	07/2020	20928	26264	5336
29	IRUGUR-DEVANGONTHI POL PIPELINE	BPCL	11/2012	02/2017	678	1472	794
30	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	4588.29	5245.96	657.67
31	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	3190.69	3375.9	185.21
32	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	ONGC	04/2019	03/2022	3228.8	3976.67	747.87
33	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTA TO 2.5 MMTA AT KANDLA, GUJARAT	IOCL	03/2018	N.A.	588.2	730.2	142
34	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	OIL	01/2018	02/2020	543.91	652.1	108.19
35	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	1112	1507.24	395.24

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
36	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	IOCL	01/2015	03/2021	1823	3027.9	1204.9
37	PARADIP HYDERABAD PIPELINE	IOCL	01/2015	12/2020	2321	3338	1017
POWER							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
38	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	9897.59	5978
39	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	19992.43	13707.1
40	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	11130.19	14719.1	3588.91
41	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	01/2018	11638.55	15105.22	3466.67
42	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	4824.12	5071.94	247.82
43	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	5867.38	2888.9
44	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	5111.33	6700	1588.67
45	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	4754.42	9129.32	4374.9
46	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II)	PGCIL	10/2016	01/2019	408.46	516.12	107.66
47	PAKRI BARWADIH COAL MINING PROJECT	NTPC	10/2004	10/2017	4237.96	4552	314.04
48	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	NTPC	01/2016	11/2020	10598.98	10997.7	398.72
49	KHARGONE STPP STAGE I (1320 MW)	NTPC	03/2015	01/2020	9870.51	11148.86	1278.35
50	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	NTPC	07/2012	08/2017	1527	1801.07	274.07
51	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	10/2017	11846	12739.82	893.82
52	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	487.49	639.46	151.97
53	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B)	PGCIL	05/2017	02/2019	445.89	675.73	229.84
54	EASTERN REGION STRENGTHENING SCHEME-XVIII	PGCIL	03/2017	07/2020	3500	3994	494
55	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	2496.9	7927.34	5430.44
56	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	2491.58	3860.35	1368.77

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
57	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	02/2017	9750.89	12176.28	2425.39
58	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	12964.6	17304	4339.4
59	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	07/2012	5353	10566	5213
60	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	14366.58	15389.42	1022.84
61	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	12/2018	12532.44	13140.91	608.47
62	TANDA TPP STAGE-II (2X660 MW)	NTPC	09/2014	07/2019	9188.98	9842.02	653.04
63	NAITWAR MORI HEP	SJVN	10/2017	12/2021	648.33	947.89	299.56
64	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	8692.97	21312.11	12619.14
65	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	1364.52	1891.41	526.89

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
66	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR	NFR	04/1983	03/2019	297.32	614	316.68
67	KODERMA-RANCHI VIA BARKAKANA (NL), ECR	ECR	03/1999	N.A.	1033.07	3550	2516.93
68	KOTLIPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	1045.2	2120.16	1074.96
69	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	M RTP	03/2000	12/2006	1049.69	3404.92	2355.23
70	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	1188.91	1619.48	430.57
71	RAMGANJMUHDI-BHOPAL (NL), WCR	WCR	04/2001	03/2021	424.6	2909.99	2485.39
72	CHHINDWARA - NAGPUR (GC)(SECR)	SECR	04/2005	N.A.	383.79	1413.76	1029.97
73	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	477.88	751.55	273.67
74	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	ECR	04/2003	N.A.	528.65	2066.78	1538.13
75	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	2393.47	5521.45	3127.98
76	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	171.1	275.08	103.98
77	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI	SR	09/2007	02/2019	724.69	2910.84	2186.15
78	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	810.78	1928.07	1117.29

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
79	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	133.41	396	262.59
80	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	1202.7	2440.53	1237.83
81	RAYADURGA-TUMKUR NL	SWR	04/2007	N.A.	2062.3	2432.5	370.2
82	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL	NR	04/2007	N.A.	336.91	791.39	454.48
83	BHANUPALI-BILASPUR BERI NL	RVNL	04/2008	12/2026	2966.99	6753.42	3786.43
84	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	287	893.45	606.45
85	GRADE SEPERATOR AT DAYABASTI	NR	04/1999	N.A.	156.65	359	202.35
86	MANUGURU-RAMAGUNDAM	SCR	04/2013	N.A.	1112	2911.84	1799.84
87	TUMKUR-CHITRADURGA-DAVENGERE NL	SWR	04/2011	N.A.	1801.01	1967	165.99
88	3RD LINE BETWEEN BHUSAWAL-JALGAON	CR	04/2011	03/2019	184.06	315	130.94
89	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	02/2012	499.96	680.68	180.72
90	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	385.2	1043	657.8
91	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	495.74	734.01	238.27
92	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	4454.17	12264.15	7809.98
93	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	2923.13	3791.66	868.53
94	NEW MAYNAGURI TO JOGIGHOPA VIA CHAGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	1180.19	4541.38	3361.19
95	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	614.45	451.58
96	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	324.73	1070	745.27
97	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	8248.5	8000.84
98	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	495.44	2980.41	2484.97
99	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP	NER	03/2007	12/2021	243.78	895	651.22
100	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP	NER	03/2013	N.A.	307	1409.09	1102.09

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
101	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	829.74	1959.74	1130
102	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	09/1995	03/2020	303.98	1720	1416.02
103	HUBLI-ANKOLA(NL), SWR	SWR	04/1997	N.A.	2315	3911.65	1596.65
104	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	393.46	1026	632.54
105	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	04/2020	511.86	2005.25	1493.39
106	MUNEERABAD-MAHABOBNAGAR(NL), SCR	SCR	04/1997	03/2000	1723	3421.35	1698.35
107	NANDYAL-YERRAGUNTLA(NL), SCR	SCR	03/1996	02/2009	164.36	1050	885.64
108	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	969.83	1312.96	343.13
109	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM)	NFR	04/2016	12/2021	602.27	2144.78	1542.51
110	DIGARU-HOJAI (102 KM)	NFR	04/2015	03/2021	870.96	1873.21	1002.25
111	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	NFR	04/2015	03/2022	2232.32	2950	717.68
112	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	701.61	810.02	108.41
113	MUZAFFARPUR-SITAMARHI NEW LINE	ECR	01/1991	07/2014	332.15	546.71	214.56
114	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM	SR	10/2013	04/2014	187.26	327	139.74
115	VIJAYAWADA-GUDUR	RVNL	04/2015	12/2023	3246.26	3548.68	302.42
116	GUNTUR-GUNTAKAL	SCR	04/2016	03/2022	3631	3887.48	256.48
117	DAUND - MANMAD (236 KM)	CR	02/2016	03/2023	1876	2081.27	205.27
118	VAIBHAVWADI -KOLHAPUR (107 KM)	CR	02/2016	03/2024	2750	3438.51	688.51
119	PUNE-NASIK (265 KM)	CR	02/2016	03/2024	2425	5341.68	2916.68
120	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	DFCC	10/2006	N.A.	11589	28181	16592
121	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	ER	04/2005	03/2017	595.51	769.4	173.89
122	PIRPAINTI-BHAGALPUR	ER	04/2011	N.A.	261.38	565	303.62
123	BANDEL-BOINCHI 3RD LINE	ER	04/2011	N.A.	288.35	502.48	214.13

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
124	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	915.98	2137.81	1221.83
125	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR	ER	04/2007	N.A.	450	1261.34	811.34
126	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	ER	04/1987	03/2006	406.99	545.7	138.71
127	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	03/2019	120.7	2172.16	2051.46
128	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	632.68	950	317.32
129	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	03/2019	314	800	486
130	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	NFR	04/1999	N.A.	819.23	1871	1051.77
131	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	03/2020	414.84	1040	625.16
132	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	373.87	132.35
133	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	03/2020	242.22	471	228.78
134	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	03/2021	906.46	4083.02	3176.56
135	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	SR	04/2007	N.A.	931.98	1121	189.02
136	MADURAI-BODINAYAKKANUR	SR	04/2008	N.A.	164.41	608.13	443.72
137	ERODE-PALANI	SR	04/2008	N.A.	288.57	1140	851.43
138	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	569.63	742	172.37
139	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	NFR	04/2010	N.A.	221.42	380	158.58
140	KUMBALAM-TURAVUR	SR	04/2011	N.A.	252.96	369.55	116.59
141	KURUPPANTHARA-CHINGAVANAM	SR	04/2007	N.A.	270.14	457.08	186.94
142	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	SR	04/1999	N.A.	198.68	559.95	361.27
143	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	SR	04/2013	N.A.	839	1500	661
144	CHENNAI-CUDDALORE VIA MAMALLAPURAM	SR	04/2008	N.A.	523.52	1205	681.48
145	ATTIPPATTU PUTTUR	SR	04/2008	02/2019	151.84	527.37	375.53
146	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	NFR	04/2013	03/2019	1798	2042.51	244.51

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
147	HAJIPUR-RAMDAYALUNAGAR DOUBLING	ECR	04/2013	N.A.	213.01	480	266.99
148	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	548	819.01	271.01
149	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	ECR	04/2004	N.A.	372.14	1470.5	1098.36
150	MOTIHARI-SITAMARHI (NL)	ECR	04/2006	N.A.	211	1006	795
151	CHHAPRA-MUZAFFARPUR (NL)	ECR	04/2006	N.A.	378.56	1858.75	1480.19
152	SAKRI-HASANPUR ROAD (NL)	ECR	04/1999	N.A.	325	735.2	410.2
153	BIHTA-AURANGABAD (NL)	ECR	04/2008	N.A.	326.2	2995.01	2668.81
154	GAYA-CHATRA (NL)	ECR	04/2008	N.A.	415.67	549.75	134.08
155	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	12/2018	258.2	358.68	100.48
156	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	651	1009	358
157	BOWAICHANDI-ARAMBAGH	SER	04/2010	N.A.	267.37	620	352.63
158	ALWAR-BANDIKUI DOUBLING	NWR	04/2013	02/2019	242.09	525	282.91
159	AJMER-BANGURGRAM	NWR	04/2011	11/2019	213.39	375	161.61
160	PUSHKAR-MERTA	NWR	04/2013	N.A.	323	432.22	109.22
161	AJMER-KOTA (NASIRABAD-JAUNDRI)	NWR	04/2013	N.A.	822	1099	277
162	THIYAT HAMIRA-SANU	NWR	04/2013	10/2018	236.93	350.45	113.52
163	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	2912.96	3845.6	932.64
164	RATLAM-DUNGARPUR VIA BANSWARA (NL)	NWR	04/2011	N.A.	2082.75	4262.36	2179.61
165	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	03/2021	1037.15	1389.05	351.9
166	PALANPUR-SAMAKHAYALI (DL)	RVNL	04/2013	12/2021	1548.66	1868.89	320.23
167	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	320.66	1378.11	1057.45
168	DHASA-JETALSAR (GC)	RVNL	04/2012	03/2021	644.38	872.65	228.27
169	AHMEDABAD-BOTAD (GC)	RVNL	04/2012	12/2021	975.62	1500	524.38

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
170	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	12/2019	246.08	395	148.92
171	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	M RTP	03/2013	03/2016	4874.58	8574.97	3700.39
172	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	295	477.31	182.31
173	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	2298.42	2733.86	435.44
174	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	3951.98	4259.48	307.5
175	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	2500	27949	25449
176	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	450	2200	1750
177	DAUSA-GANGAPUR CITY(NL), NWR	NWR	02/1997	02/2019	410.08	860.41	450.33
178	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	8600	7260.52
179	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	2326.52	6911	4584.48
180	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	532.87	2145	1612.13
181	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN	NFR	02/1999	04/2010	380.6	1090.6	710
182	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM	WR	04/2017	03/2020	691.84	1017.91	326.07
183	JALANDHAR-PATHANKOT-JAMMU TAWI	NR	03/2002	03/2016	625	859	234
184	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	2288	4970.11	2682.11
185	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	WR	02/1991	03/2019	551.51	890.76	339.25
186	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	644.78	998	353.22
187	JHARSUGUDA-BILASPUR 4TH LINE	SECR	04/2015	03/2021	1973	2135.34	162.34
188	CHAMPA-JHARSUGUDA 3RD LINE	SECR	04/2008	12/2019	872	1226.51	354.51
189	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	229	1096	867
190	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	ECR	04/1991	N.A.	329.39	1483.14	1153.75
191	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR	ECR	04/1998	N.A.	180.82	726.31	545.49
192	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	731.64	1185.73	454.09

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
193	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	744.04	1215.54	471.5
194	BURHWAL - GONDA - 3RD RUNNING LINE.	NER	04/2016	N.A.	602.5	714.34	111.84
195	CHANDIGARH-BADDI	NR	04/2007	03/2023	328.14	1540.13	1211.99
196	WESTERN DEDICATED FREIGHT CORRIDOR	DFCC	11/2007	03/2020	16592	51101	34509
197	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE	NER	04/2017	01/2018	1343	1476.15	133.15
198	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	SR	02/2015	03/2020	760	1536	776
199	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	SR	02/1996	03/2005	268.87	950	681.13
200	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	585.93	1268.32	682.39
201	MANMAD-PARBHANI-NANDED-SECUNDERABAD- GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	SCR	04/2017	03/2022	119.73	449.39	329.66
202	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	1908.51	3524.81	1616.3
203	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	582.13	1247.64	665.51
204	BINA - KOTA DOUBLING WITH RE	RVNL	04/2011	12/2020	1485.85	1835.83	349.98
205	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	RVNL	03/2012	12/2020	1183.25	1825	641.75
206	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	942.95	1536	593.05
207	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	948.04	2009	1060.96
208	VIZIANAGARAM -SAMABALPUR 3RD LINE	RVNL	01/1991	12/2024	2335.67	3327.72	992.05
209	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	713.48	2725	2011.52
210	RISHIKESH - KARNAPRAYAG NEW LINE	RVNL	04/2011	12/2024	16216	22716.11	6500.11
211	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	927.01	1400	472.99
212	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	1027.4	2373	1345.6
213	TURAVUR-AMBALAPUZHA DOUBLING	SR	02/2015	N.A.	1000	1246	246
214	ANGAMALI-SABARIMALA (N.L.)(SR)	SR	10/1998	N.A.	1566	2815.62	1249.62
215	KODERMA-TILAIYA (NL), ECR	ECR	04/2002	N.A.	459.91	1625.87	1165.96

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
216	HAJIPUR - BACHAWARA	ECR	05/2015	03/2019	678.54	929.86	251.32
217	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	1614.59	1870.41	255.82
218	ARSIKERE-TUMKUR	SWR	03/2015	03/2020	578	783	205
219	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	NWR	05/2015	N.A.	873.71	1980.21	1106.5
220	SAMASTIPUR-DARBANGHA	ECR	05/2015	N.A.	380	519.33	139.33
221	YELAHANKA-PENUKONDA	SWR	05/2015	03/2020	860.43	1147	286.57
222	PHULERA - DIGANA DOUBLING	NWR	05/2015	03/2020	600	701.81	101.81
223	HUBLI- CHIKJAJUR	SWR	03/2015	03/2020	1156.94	1656	499.06
224	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	SER	04/2012	12/2016	148.77	377	228.23
225	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	1111.99	1539.28	427.29
226	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	1503.71	3377	1873.29
227	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	2271.5	4517.49	2245.99
228	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	RVNL	04/2010	03/2023	2127	3000	873
229	QADIAN-BEAS	NR	04/2011	N.A.	205.22	841.9	636.68
230	HARIDWAR-LAKSAR	NR	04/2012	N.A.	219.83	346.63	126.8
231	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	SCR	04/2008	03/2014	2132.77	3037.95	905.18
232	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	03/2020	704.31	927.94	223.63
233	NADIKUDE-SRI KALAHASTI	SCR	04/2011	03/2021	2288.7	2643.25	354.55
234	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE	NR	04/2012	N.A.	295.68	419	123.32
235	BOINCHI-SHAKTIGARH 3RD LINE	ER	04/2011	N.A.	175.8	495.1	319.3
236	HANSDIHA-GODDA NL	ER	04/2011	03/2020	542.18	663.13	120.95
237	TARAKESHWAR-MAGRA NEW BG LINE	ER	04/2010	N.A.	365.17	527.54	162.37
238	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	792.89	1377.48	584.59

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
239	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	3503.69	5912.4	2408.71
240	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	2913.51	4639	1725.49
241	ETAWAH-MAINPURI (NL),NCR	NCR	04/1997	12/2008	120	346	226
242	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	607.09	1425.44	818.35
243	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	12/2017	1185.64	1844.47	658.83
ROAD TRANSPORT AND HIGHWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
244	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	NHAI	12/2003	02/2009	280	520	240
245	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	1108	2967.5	1859.5
246	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	196	655.17	459.17
247	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	MORTH	11/2010	03/2011	624.41	992.67	368.26
248	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MORTH	08/2010	10/2010	193.69	327.92	134.23
249	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	MORTH	04/2013	08/2013	151.59	370.01	218.42
250	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	MORTH	01/2013	02/2013	182.28	369.64	187.36
251	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1	MORTH	12/2010	01/2019	169.26	299	129.74
252	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	MORTH	01/2016	10/2016	624.98	731.5	106.52
253	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM	NHAI	12/2017	N.A.	217.96	884	666.04
254	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V	NHAI	12/2017	N.A.	656.98	840	183.02
255	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF	NHAI	03/2018	N.A.	1029.96	1261.05	231.09
256	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)	NHAI	03/2018	03/2021	1532.62	2499	966.38
257	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF	NHAI	02/2018	N.A.	1052.21	1449	396.79
258	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C	NHAI	03/2018	N.A.	1120.57	1332	211.43
259	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR.	NHAI	03/2018	N.A.	925.4	1197	271.6
260	REHABILITATION AND UP GRADATION TO FOUR	NHAI	03/2018	N.A.	1261.98	1952.2	690.22

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
	LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA)						
261	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA	NHAI	02/2018	N.A.	2177.8	2450	272.2
262	SIX-LANING OF BANGALORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT	NHAI	02/2018	N.A.	1995.34	2400	404.66
263	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU	NHAI	02/2018	N.A.	1166.26	1296.93	130.67
264	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH	NHAI	02/2018	N.A.	1424.77	1853.42	428.65
265	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	1124.11	1232.76	108.65
266	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	NHAI	09/2016	08/2019	950.69	1108	157.31
267	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (	NHAI	09/2016	N.A.	1239.82	1727.66	487.84
268	4 LANING FROM PHAGWARA TO RUPNAGAR	NHAI	08/2016	N.A.	1169.61	2280	1110.39
269	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	NHAI	08/2016	09/2019	1388.34	2587.5	1199.16
270	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ	NHAI	08/2015	N.A.	854.8	1038.56	183.76
271	SIX-LANING OF BARWA ADDA-PANAGARH	NHAI	04/2014	N.A.	1665	2360.65	695.65
272	FOUR LANING OF CHANDIGARH - KHARAR	NHAI	10/2015	12/2017	447.29	746.43	299.14
273	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	11/2015	1055	1601.77	546.77
274	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	NHAI	12/2015	06/2018	1083	1827.15	744.15
275	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	531.13	730.97	199.84
276	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	MORTH	08/2010	10/2010	195.04	377.99	182.95
277	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	MORTH	11/2011	09/2015	954.43	1191.51	237.08
278	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	MORTH	11/2010	02/2011	470.2	630.36	160.16
279	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	NHAI	03/2016	04/2019	1587.49	2982	1394.51
280	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION	NHAI	02/2016	03/2019	997.15	1115.95	118.8
281	MEERUT-BULANDSHAHR	NHAI	01/2016	N.A.	683.24	987.94	304.7
282	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR	NHAI	08/2015	04/2018	516.13	649.27	133.14

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
283	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	1266.6	1544	277.4
284	BRAHMPUTRA BRIDGE, NH NO-31	NHAI	12/2003	04/2010	217.61	360.84	143.23
285	INDORE-DEWAS(NH-3)	NHAI	11/2010	05/2013	325	475	150
286	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM.	MoRTH	04/2013	08/2013	166.27	359.92	193.65
287	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	MoRTH	03/2012	05/2012	207.03	389.45	182.42
288	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	MoRTH	12/2011	02/2012	156.63	276	119.37
289	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	199.81	340.14	140.33
290	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	NHAI	12/2003	11/2008	167.64	435.78	268.14
291	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MoRTH	08/2010	09/2014	186.96	322.24	135.28
292	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH	MoRTH	10/2013	03/2017	445.89	653.29	207.4
293	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7	MoRTH	04/2014	08/2017	279.7	398.52	118.82
294	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A 0	MoRTH	08/2014	11/2017	823.2	937.76	114.56
295	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 0	MoRTH	08/2014	11/2017	600.87	720.97	120.1
296	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4	NHAI	03/2018	N.A.	642.13	807	164.87
297	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA	NHAI	03/2018	N.A.	634.7	931.21	296.51
298	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N	NHAI	03/2018	N.A.	2065.96	2169	103.04
299	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(0	NHAI	03/2017	03/2020	993.16	1434	440.84
300	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	NHAI	03/2017	03/2020	831.58	1177	345.42
301	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	NHAI	03/2017	03/2020	2064.99	2447	382.01
302	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	1288.07	1420	131.93
303	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	NHAI	03/2017	03/2020	1041.62	1187.1	145.48
304	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	NHAI	03/2017	03/2020	744.64	982	237.36
305	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	NHAI	03/2017	03/2020	1184.71	1310	125.29

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
306	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	NHAI	11/2012	07/2018	605.84	722.46	116.62
307	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	MoRTH	11/2010	05/2017	268.08	390.73	122.65
308	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	MoRTH	11/2013	05/2017	497.05	881.05	384
309	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270	MoRTH	10/2013	03/2017	445.89	653.29	207.4
310	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI	NHAI	04/2014	01/2016	495.78	627.93	132.15
311	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	1928.22	3182.34	1254.12
312	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	NHAI	07/2012	01/2014	291.36	469.31	177.95
313	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	2848	3379.45	531.45
314	NASHRI- CHANANI	NHAI	05/2011	06/2015	2159	2519	360
315	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	155.04	255.23	100.19

STEEL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
316	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	15525	21940	6415

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
317	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	13334	24664	11330

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
318	BANGALORE METRO RAIL PROJECT PHASE-2	BMRL	02/2014	02/2019	26405.14	30695.12	4289.98
319	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRL	07/2013	01/2015	23136	33406	10270
320	AHMEDABAD METRO RAIL PROJECT PHASE 1	MEGA	11/2014	12/2018	10773	12787	2014
321	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	114.26	266	151.74
322	REDEVELOPMENT OF EAST KIDWAI NAGAR	NBCC	06/2012	11/2019	4264	4720.73	456.73
323	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	14600	19058	4458

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
324	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	5181.79	6218.14	1036.35
WATER RESOURCES							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
325	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	10151.04	55548.87	45397.83

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(APRIL 2021)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	03/2023	1,2320.00	1,7079.00	4759	75
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	02/2022	1,1459.00	1,6580.00	5121	74
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2022	3492.00	6840.00	3348	145

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2021	417.23	707.73	290.5	33

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
5	BHATADI EXPANSION OC MINE	WCL	02/2016	03/2019	09/2026	304.52	729.86	425.34	90
6	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2022	152.43	459.49	307.06	84
7	NEW MAJRI UG TO OC	WCL	05/2015	03/2019	09/2026	295.56	496.38	200.82	90
8	AMALGAMATED GONDEGAON GHATROHAN OC	WCL	02/2016	03/2019	03/2022	198.68	325.18	126.5	36
9	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2022	162.76	349.28	186.52	84

DPIIT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
10	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	IICC	11/2017	12/2019	12/2021	4773.00	5178.00	405	24
11	DELHI MUMBAI INDUSTRIAL CORRIDOR	DMIC	09/2011	09/2019	07/2021	1,2579.09	1,3812.30	1233.21	22

HOME AFFAIRS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
12	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	12/2021	1219.21	2000.00	780.79	26

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

466

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(APRIL 2021)

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
13	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	ONGC	04/2019	03/2022	05/2023	3228.80	3976.67	747.87	14
14	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	HPCL	09/2017	06/2021	08/2022	2677.00	3072.00	395	14
15	VISAKH REFINERY MODERNISATION PROJECT	HPCL	07/2016	07/2020	07/2022	2,0928.00	2,6264.00	5336	24
16	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	02/2022	4497.00	6025.00	1528	38
17	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	02/2022	1112.00	1507.24	395.24	32
18	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	OIL	01/2018	02/2020	06/2021	543.91	652.10	108.19	16
19	IRUGUR-DEVANGONTHI POL PIPELINE	BPCL	11/2012	02/2017	08/2022	678.00	1472.00	794	66
20	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	05/2022	3190.69	3375.90	185.21	49
21	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	02/2022	2915.00	5909.00	2994	110
22	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	03/2022	607.06	1236.00	628.94	53
23	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	IOCL	01/2015	03/2021	12/2021	1823.00	3027.90	1204.9	9
24	PARADIP HYDERABAD PIPELINE	IOCL	01/2015	12/2020	03/2022	2321.00	3338.00	1017	15
25	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	02/2022	861.79	2001.00	1139.21	105
26	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	05/2021	4588.29	5245.96	657.67	33

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
27	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	12/2021	5111.33	6700.00	1588.67	36
28	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	07/2023	8692.97	2,1312.11	12619.1	141

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

467

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
29	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	NTPC	01/2016	11/2020	07/2022	1,0598.98	1,0997.70	398.72	20
30	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	03/2024	4754.42	9129.32	4374.9	63
31	EASTERN REGION STRENGTHENING SCHEME-XVIII	PGCIL	03/2017	07/2020	06/2021	3500.00	3994.00	494	11
32	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	12/2021	1,2964.60	1,7304.00	4339.4	43
33	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	07/2022	3919.59	9897.59	5978	154
34	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	08/2023	6285.33	1,9992.43	13707.1	155
35	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	08/2022	1,1130.19	1,4719.10	3588.91	108
36	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2022	2978.48	5867.38	2888.9	117
37	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	12/2018	05/2021	1,2532.44	1,3140.91	608.47	29
38	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	10/2022	1,4366.58	1,5389.42	1022.84	40
39	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	07/2012	07/2021	5353.00	1,0566.00	5213	108
40	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2023	2491.58	3860.35	1368.77	126

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
41	JALANDHAR-PATHANKOT-JAMMU TAWI	NR	03/2002	03/2016	06/2021	625.00	859.00	234	63
42	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	12/2023	2288.00	4970.11	2682.11	21
43	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	WR	02/1991	03/2019	10/2021	551.51	890.76	339.25	31
44	JHARSUGUDA-BILASPUR 4TH LINE	SECR	04/2015	03/2021	12/2023	1973.00	2135.34	162.34	33

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

468

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
45	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	06/2022	731.64	1185.73	454.09	15
46	CHANDIGARH-BADDI	NR	04/2007	03/2023	03/2025	328.14	1540.13	1211.99	24
47	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	NFR	04/2015	03/2022	03/2023	2232.32	2950.00	717.68	12
48	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	12/2021	969.83	1312.96	343.13	21
49	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	03/2030	1027.40	2373.00	1345.6	324
50	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	06/2022	927.01	1400.00	472.99	39
51	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	12/2021	713.48	2725.00	2011.52	21
52	VIZIANAGARAM -SAMABALPUR 3RD LINE	RVNL	01/1991	12/2024	12/2026	2335.67	3327.72	992.05	24
53	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	12/2021	948.04	2009.00	1060.96	21
54	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	06/2022	942.95	1536.00	593.05	39
55	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	RVNL	03/2012	12/2020	12/2022	1183.25	1825.00	641.75	24
56	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	12/2023	4454.17	1,2264.15	7809.98	153
57	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	MRTP	04/2006	06/2013	12/2021	495.74	734.01	238.27	102
58	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	03/2023	385.20	1043.00	657.8	48
59	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	03/2024	532.87	2145.00	1612.13	60
60	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	12/2024	2326.52	6911.00	4584.48	117
61	DAUSA-GANGAPUR CITY(NL),NWR	NWR	02/1997	02/2019	06/2022	410.08	860.41	450.33	40

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

469

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
62	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	03/2024	450.00	2200.00	1750	140
63	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2022	2500.00	2,7949.00	25449	241
64	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	03/2025	3951.98	4259.48	307.5	108
65	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	SR	09/2007	02/2019	03/2025	724.69	2910.84	2186.15	73
66	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	03/2023	2393.47	5521.45	3127.98	108
67	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	07/2021	477.88	751.55	273.67	112
68	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	03/2025	2913.51	4639.00	1725.49	108
69	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	03/2024	3503.69	5912.40	2408.71	24
70	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	03/2023	792.89	1377.48	584.59	24
71	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	02/2012	03/2025	499.96	680.68	180.72	157
72	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	06/2021	287.00	893.45	606.45	114
73	NADIKUDE-SRI KALAHASTI	SCR	04/2011	03/2021	03/2024	2288.70	2643.25	354.55	36
74	KOTLIPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2024	1045.20	2120.16	1074.96	180
75	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	03/2025	1188.91	1619.48	430.57	72
76	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	03/2024	607.09	1425.44	818.35	133
77	RAMGANJMUNDI-BHOPAL (NL), WCR	WCR	04/2001	03/2021	03/2023	424.60	2909.99	2485.39	24
78	SUKINDA ROAD - ANGUL (NL) (ECOR)	RVNL	04/1998	02/2015	06/2022	1202.70	2440.53	1237.83	88
79	TALCHER-BIMALAGARH(NL) (ECOR)	ECOR	04/2005	06/2021	03/2025	810.78	1928.07	1117.29	45

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

470

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
80	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	03/2020	06/2021	704.31	927.94	223.63	15
81	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	SCR	04/2008	03/2014	03/2027	2132.77	3037.95	905.18	156
82	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	03/2023	2271.50	4517.49	2245.99	24
83	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	03/2022	495.44	2980.41	2484.97	216
84	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2025	247.66	8248.50	8000.84	202
85	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	11/2022	324.73	1070.00	745.27	128
86	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	05/2021	1180.19	4541.38	3361.19	149
87	KHURDA ROAD-BOLANGIR(NL) ECR	ECR	04/1994	03/2009	03/2026	2923.13	3791.66	868.53	204
88	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	2733.86	435.44	141
89	MUNEERABAD-MAHABOBNAGAR(NL), SCR	SCR	04/1997	03/2000	03/2023	1723.00	3421.35	1698.35	276
90	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	04/2020	04/2021	511.86	2005.25	1493.39	12
91	TIRUCHIRAPPALI-NAGORE-KARAIKKAL (SR) (GC)	SR	09/1995	03/2020	03/2025	303.98	1720.00	1416.02	60
92	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	03/2024	829.74	1959.74	1130	48
93	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	03/2022	1503.71	3377.00	1873.29	24
94	SAMBALPUR-TALCHER DOUBLING	ECR	03/2011	02/2019	12/2021	1111.99	1539.28	427.29	34
95	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	02/2022	295.00	477.31	182.31	37
96	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	M RTP	03/2013	03/2016	06/2021	4874.58	8574.97	3700.39	63

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

471

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
97	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	03/2023	320.66	1378.11	1057.45	48
98	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	03/2021	12/2021	1037.15	1389.05	351.9	9
99	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	12/2024	2912.96	3845.60	932.64	33
100	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	03/2025	651.00	1009.00	358	120
101	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	12/2018	04/2021	258.20	358.68	100.48	28
102	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	03/2023	548.00	819.01	271.01	36
103	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	NFR	04/2013	03/2019	03/2024	1798.00	2042.51	244.51	60
104	HUBLI- CHIKJAJUR	SWR	03/2015	03/2020	03/2023	1156.94	1656.00	499.06	36
105	PHULERA - DIGANA DOUBLING	NWR	05/2015	03/2020	10/2022	600.00	701.81	101.81	31
106	YELAHANKA-PENUKONDA	SWR	05/2015	03/2020	06/2021	860.43	1147.00	286.57	15
107	ARSIKERE-TUMKUR	SWR	03/2015	03/2020	06/2021	578.00	783.00	205	15
108	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	03/2024	1614.59	1870.41	255.82	60
109	HAJIPUR - BACHAWARA	ECR	05/2015	03/2019	05/2021	678.54	929.86	251.32	26
110	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	03/2022	569.63	742.00	172.37	24
111	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2021	632.68	950.00	317.32	69
112	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	03/2019	12/2027	120.70	2172.16	2051.46	105
113	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-	ER	04/1987	03/2006	03/2025	406.99	545.70	138.71	228

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

472

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	BUDAKHALI AND CHANDRANAG								
114	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	03/2025	915.98	2137.81	1221.83	36
115	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	ER	04/2005	03/2017	03/2025	595.51	769.40	173.89	96
116	GUNTUR-GUNTAKAL	SCR	04/2016	03/2022	03/2024	3631.00	3887.48	256.48	24
117	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	03/2024	701.61	810.02	108.41	64
118	BINA - KOTA DOUBLING WITH RE	RVNL	04/2011	12/2020	12/2021	1485.85	1835.83	349.98	12
119	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	03/2023	582.13	1247.64	665.51	12
120	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	12/2023	1908.51	3524.81	1616.3	9
121	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE-GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	SCR	04/2017	03/2022	12/2022	119.73	449.39	329.66	9
122	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	12/2021	585.93	1268.32	682.39	34
123	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	SR	02/1996	03/2005	09/2021	268.87	950.00	681.13	198
124	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	SR	02/2015	03/2020	06/2022	760.00	1536.00	776	27
125	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	03/2024	744.04	1215.54	471.5	36
126	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	12/2024	229.00	1096.00	867	36
127	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	03/2025	644.78	998.00	353.22	96

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
128	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	MoRTH	01/2016	10/2016	06/2021	624.98	731.50	106.52	56
129	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT	MoRTH	08/2010	09/2014	06/2021	186.96	322.24	135.28	81

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

473

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	KALADAN MULTI MOD								
130	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	06/2021	531.13	730.97	199.84	37
131	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	06/2021	1288.07	1420.00	131.93	15
132	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	MoRTH	04/2013	08/2013	06/2021	151.59	370.01	218.42	94
133	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	12/2022	2848.00	3379.45	531.45	105
134	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MoRTH	08/2010	10/2010	06/2021	193.69	327.92	134.23	128
135	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM.	MoRTH	04/2013	08/2013	06/2021	166.27	359.92	193.65	94
136	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	MoRTH	01/2013	02/2013	06/2021	182.28	369.64	187.36	100
137	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	MoRTH	08/2010	10/2010	06/2021	195.04	377.99	182.95	128
138	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	05/2021	1124.11	1232.76	108.65	44
139	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	MoRTH	11/2013	05/2017	04/2021	497.05	881.05	384	47
140	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	MoRTH	11/2011	09/2015	10/2021	954.43	1191.51	237.08	73
141	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	06/2021	1928.22	3182.34	1254.12	74
142	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH	MoRTH	10/2013	03/2017	04/2021	445.89	653.29	207.4	49

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
143	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	07/2021	1,5525.00	2,1940.00	6415	74

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
144	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	07/2021	1,3334.00	2,4664.00	11330	72

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

474

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(APRIL 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
145	AHMEDABAD METRO RAIL PROJECT PHASE 1	MEGA	11/2014	12/2018	08/2022	1,0773.00	1,2787.00	2014	44
146	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	01/2015	03/2023	2,3136.00	3,3406.00	10270	98
147	BANGALORE METRO RAIL PROJECT PHASE-2	BMRCL	02/2014	02/2019	06/2024	2,6405.14	3,0695.12	4289.98	64

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
148	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	04/2022	1,0151.04	5,5548.87	45397.8	25

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

COR -> Cost Overrun

List of projects original without Date of Commissioning

Costing Rs. 150 Crore and above						(April 2021)			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
1	<u>COAL</u> <u>Singareni Colliers Company Limited</u> SRP OC-II EXPANSION PROJECT - [N06000173]SCCL, TELANGANA Total	11/2016	272.73 - 272.73 -	272.73 - 272.73 -	153.75 - 153.75 -	- - - -	03/2022	-	2/6 2/6
2	<u>HEALTH AND FAMILY WELFARE</u> <u>Hospital Services Consultancy Corporation Ltd</u> GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC, DELHI	12/2017	156.56 -	190.34 -	143.14 -	- -	06/2021	-	0/0
3	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC, ANDHRA PRADESH	03/2018	601.02 -	601.02 -	400.25 -	- -	06/2021	-	0/0
4	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC, MAHARASHTRA	03/2018	582.99 -	582.99 -	482.32 -	- -	06/2021	-	0/0
5	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC, WEST BENGAL	04/2018	651.99 -	651.99 -	503.55 -	- -	06/2021	-	0/0
	Total		1,992.56 -	2,026.34 -	1,529.26 -				0/0
6	<u>RAILWAYS</u> <u>East Central Railways</u> KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR, JHARKHAND	03/1999	1,033.07 -	3,550.00 -	3,567.20 -	- -	03/2022	-	0/0
7	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIAWAN-BIHARSHARIF, - [N22000476]ECR, BIHAR	04/1991	329.39 -	1,483.14 -	1,207.52 -	- -	03/2022	-	0/0
8	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR, BIHAR	04/2003	528.65 -	2,066.78 -	1,560.44 -	- -	03/2023	-	0/0
9	KODERMA-TILAIYA (NL), ECR - [220100305]ECR, JHARKHAND	04/2002	459.91 -	1,625.87 -	758.44 -	- -	03/2023	-	0/0
10	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR, BIHAR	04/2006	378.56 -	1,858.75 -	386.35 -	- -	03/2023	-	0/0
11	ARARIA-SUPAUL (NL) - [N22000177]ECR, BIHAR	04/2008	1,605.17 -	1,605.17 -	53.52 -	- -	03/2023	-	0/0
12	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR, BIHAR	04/2004	372.14 -	1,470.50 -	1,288.24 -	- -	03/2023	-	0/0
13	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR, BIHAR	04/1997	162.87 -	614.45 -	348.95 -	- -	12/2023	-	0/0

Costing Rs. 150 Crore and above (April 2021)									
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
14	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR	04/2008	326.20	2,995.01	2.08	-	03/2024	-	0/0
15	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05	228.05	1.53	-	03/2024	-	0/0
16	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00	519.33	282.65	-	03/2025	-	0/0
	<u>Eastern Railways</u>								
17	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80	495.10	288.51	-	03/2022	-	0/0
18	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64	272.20	261.26	-	03/2022	-	0/0
19	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93	310.70	293.10	-	03/2024	-	0/0
20	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00	1,261.34	-	-	03/2025	-	0/0
21	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03	260.10	11.74	-	03/2025	-	0/0
22	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56	174.56	71.43	-	03/2025	-	0/0
23	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55	250.55	20.11	-	03/2025	-	0/0
24	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17	527.54	1.76	-	03/2025	-	0/0
25	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47	298.22	52.09	-	03/2025	-	0/0
26	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96	336.96	70.20	-	03/2025	-	0/0
27	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89	166.89	.02	-	03/2025	-	0/0
	<u>Metropolitan Rapid Transport Projects</u>								
28	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSHUPUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78	268.52	.03	-	03/2025	-	0/0
	<u>North East Frontier Railway</u>								
29	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52	373.87	287.09	-	12/2021	-	0/0
	<u>North Eastern Railway</u>								
30	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH	04/2016	602.50	714.34	40.34	-	12/2023	-	0/0
	<u>Northern Railway</u>								

Costing Rs. 150 Crore and above (April 2021)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
31	DEOBAND (MUZAFFARNAGAR)-ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91	791.39	572.99	-	03/2023	-	0/0
32	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	1,229.00	1,265.00	103.72	-	03/2023	-	0/0
33	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68	419.00	127.91	-	09/2023	-	0/0
34	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65	359.00	111.51	-	03/2024	-	0/0
35	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22	841.90	1.73	-	03/2024	-	0/0
<u>South Eastern Railway</u>									
36	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37	620.00	40.99	-	03/2025	-	0/0
<u>South Western Railway</u>									
37	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01	1,967.00	71.56	-	12/2023	-	0/0
38	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00	558.00	-	-	12/2023	-	0/0
39	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00	296.10	.01	-	12/2023	-	0/0
40	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	348.85	348.85	.36	-	12/2023	-	0/0
41	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75	167.50	.34	-	12/2023	-	0/0
42	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25	327.25	-	-	12/2023	-	0/0
43	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00	3,911.65	157.01	-	12/2024	-	0/0
44	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	2,062.30	2,432.50	1,127.71	-	03/2025	-	2/2
<u>Southern Railway</u>									
45	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14	457.08	439.49	-	12/2021	-	0/0
46	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52	1,205.00	2.28	-	03/2024	-	0/0
47	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68	559.95	52.50	-	03/2024	-	0/0
48	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83	582.83	239.49	-	12/2025	-	0/0
Total			22,239.97	40,837.94	13,904.20				2/2
<u>ROAD TRANSPORT AND HIGHWAYS</u>									
<u>Ministry Of Road Transport And Highways (State Pwds)</u>									
49	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH	11/2016	326.99	326.99	105.89	-	09/2021	-	0/0

Costing Rs. 150 Crore and above (April 2021)									
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
50	<u>National Highways And Infrastructure Development Corporation Ltd.</u> WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA	04/2017	553.51 -	553.51	75.51	- -	09/2021	-	2/4
51	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH	02/2017	175.06 -	175.06	82.18	- -	04/2022	-	2/4
52	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL,ARUNACHAL PRADESH	02/2017	176.12 -	176.12	67.95	- -	04/2022	-	2/4
53	<u>National Highways Authority Of India</u> SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA	03/2018	806.11 -	806.11	189.70	- -	04/2021	-	0/0
54	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	392.00	353.42	- -	04/2021	-	0/0
55	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA	01/2018	621.00 -	621.00	591.21	- -	04/2021	-	2/3
56	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	1,244.10	1,590.00	- -	05/2021	-	0/0
57	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH	03/2018	478.74 -	478.74	127.42	- -	05/2021	-	0/0
58	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	1,008.96	930.39	- -	06/2021	-	0/0
59	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	686.65	227.63	- -	06/2021	-	0/0
60	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	417.51	127.61	- -	06/2021	-	0/0
61	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	668.86	276.59	- -	06/2021	-	0/0
62	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	686.65	261.74	- -	06/2021	-	0/0

Costing Rs. 150 Crore and above (April 2021)									
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
63	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	1,522.00	304.40	- -	06/2021	-	0/0
64	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141) - [N24000738]NHAI,ODISHA	01/2018	999.00 -	999.00	102.70	- -	06/2021	-	0/0
65	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	503.88	25.40	- -	06/2021	-	0/0
66	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT	03/2018	2,702.05 -	2,043.00	1,327.65	- -	06/2021	-	0/0
67	FOUR LANNING OF LUDHIYANA-TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	479.00	456.80	- -	07/2021	-	0/0
68	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA	11/2016	1,071.61 -	1,048.10	965.72	- -	07/2021	-	3/4
69	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	1,323.15	785.33	- -	07/2021	-	0/0
70	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI,WEST BENGAL	03/2018	1,261.98 -	1,952.20	934.06	- -	07/2021	-	0/0
71	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB	02/2018	261.76 -	207.00	200.74	- -	07/2021	-	0/0
72	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64 -	1,437.64	564.11	- -	07/2021	-	0/0
73	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA	03/2018	634.70 -	931.21	268.17	- -	07/2021	-	0/0
74	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA	03/2018	795.50 -	799.30	213.17	- -	07/2021	-	0/0
75	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 -	1,162.92	58.20	- -	07/2021	-	0/0
76	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27 -	950.27	224.81	- -	08/2021	-	3/4

Costing Rs. 150 Crore and above (April 2021)									
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
77	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA	01/2018	607.00 -	607.00	440.92	- -	08/2021	-	0/1
78	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	614.48	217.40	- -	08/2021	-	0/0
79	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	564.66	240.00	- -	08/2021	-	0/1
80	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26 -	1,296.93	220.78	- -	08/2021	-	0/0
81	FOUR LANING OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35 -	505.35	243.30	- -	08/2021	-	0/0
82	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	1,031.95	374.05	- -	09/2021	-	0/0
83	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 -	1,550.98	1,401.00	- -	09/2021	-	0/0
84	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	825.17	512.04	- -	10/2021	-	2/4
85	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 -	1,959.00	1,211.72	- -	10/2021	-	0/0
86	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 -	2,400.00	3,088.59	- -	11/2021	-	0/0
87	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	1,117.84	-	- -	12/2021	-	0/0
88	FOUR LANING OF MADURAI-CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	628.71	310.06	- -	12/2021	-	0/0
89	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI,MADHYA PRADESH	10/2019	743.88 -	743.89	298.54	- -	12/2021	-	0/3

Costing Rs. 150 Crore and above (April 2021)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
90	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU	03/2018	1,016.92 -	1,071.00	218.47	- -	01/2022	-	0/0
91	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA - [N24001213]NHAI,MADHYA PRADESH	12/2017	1,094.97 -	1,094.97	-	- -	02/2022	-	2/4
92	FOUR LANING WITH PS TALEBANI - SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	752.28	213.52	- -	03/2022	-	0/1
93	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	953.09	332.04	- -	03/2022	-	0/0
94	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43 -	314.43	85.61	- -	03/2022	-	0/0
95	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]NHAI,MADHYA PRADESH	12/2017	656.98 -	840.00	105.50	- -	11/2022	-	0/4
	Total		41,408.44 -	42,472.66	20,952.04				18/41
	<u>URBAN DEVELOPMENT</u> <u>National Building Construcion Corporation Ltd</u>								
96	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI	07/2016	2,694.00 -	2,694.00	744.73	- -	12/2022	-	0/9
	Total		2,694.00 -	2,694.00	744.73				0/9
	Grand Total		68,607.70	88,303.67	37,283.98				22/58

List of Projects on schedule w.r.t. Latest Schedule

Annexure - XII

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
1	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	7/2018	346.27 -	480.33	51.11	09/2021 -	09/2021
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT - [N04000079]	3/2017	475.39 -	475.39	88.11	04/2021 -	04/2021
3	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA - [N04000081]	1/2019	389.71 -	389.71	140.62	11/2021 10/2022	10/2022
4	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA - [N04000080]	1/2016	458.00 -	458.00	135.60	03/2020 12/2021	12/2021
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]	12/2016	1,142.00 -	1,232.00	368.37	03/2021 03/2022	03/2022
6	CO CIVIL AVIATION RESEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD [N04000086]	5/2020	353.61 -	353.61	61.13	05/2022 -	05/2022
7	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT [N04000091]	4/2020	611.80 -	611.80	21.25	03/2023 -	03/2023
8	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT - [N04000088]	1/2018	1,405.00 -	1,405.00	250.63	08/2022 -	08/2022
	Total		5,181.78 -	5,405.84	1,116.82		
	<u>COAL</u>						
	<u>Central Coal Fields Limited</u>						
9	MAGADH EXPANSION OC(51 MTY) - [N06000015]	8/2008	6,964.33 6,964.33	706.40	706.20	07/2012 03/2025	03/2025
10	NORTH URIMARI EXPANSION OCP - [N06000182]	3/2019	1,553.06 -	1,553.06	277.47	03/2023 -	03/2023
11	TETARIAKHAR EXPANSION OCP - [N06000186]	11/2019	243.52 -	243.52	39.79	03/2023 -	03/2023
12	RECAST EPR AMRAPALI OC - [N06000103]	2/2012	4,983.58 4,983.58	4,983.58	245.85	03/2020 03/2024	03/2024
	<u>Eastern Coal Fields Limited</u>						
13	EXPANSION PR OF JHANJRA UG(5.00 MTY) - [N06000020]	11/2015	1,210.12 -	1,210.12	26.05	03/2022 03/2029	03/2029
14	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT - [N06000191]	4/2020	483.65 -	483.65	1.82	03/2025 -	03/2025
15	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	247.51	03/2022 -	03/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
16	NAKRAKONDA KUMARDIH B OCP - [N06000170]	8/2018	502.68 -	502.68	12.62	03/2029 -	03/2029
17	TILABONI UG MINE - [N06000172]	2/2019	916.62 -	916.62	.61	03/2027 -	03/2027
18	PARASEA- BELBAID REORGANISATION UG MINE - [N06000185]	7/2019	826.42 -	826.42	.03	03/2027 -	03/2027
19	CHITRA EAST (RCE) OCP - [N06000169]	8/2018	513.98 -	513.98	121.23	03/2024 -	03/2024
20	SIDULI MINE (OC AND UG) - [N06000165]	5/2018	535.18 -	535.18	1.39	03/2026 -	03/2026
	<u>Mahanadi Coal Fields Limited</u>						
21	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	1,986.09	03/2026 -	03/2026
22	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY) - [N06000035]	12/2007	8,416.19 8,416.19	8,416.19	890.78	03/2013 03/2028	03/2028
23	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]	11/2018	2,838.87 -	2,838.87	1,236.90	03/2029 -	03/2029
24	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]	5/2018	2,434.75 -	2,434.75	181.04	03/2027 -	03/2027
25	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY) - [N06000044]	12/2007	3,504.21 3,504.21	3,504.21	607.83	03/2010 03/2029	03/2029
	<u>Neyveli Lignite Corporation</u>						
26	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]	4/2013	1,458.17 -	709.06	484.81	06/2015 03/2025	03/2025
27	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	11,574.21	11/2021 07/2022	07/2022
	<u>Northern Coal Fields Limited</u>						
28	SEMARIA OPENCAST PROJECT - [N06000176]	5/2019	396.58 -	396.58	-	03/2026 -	03/2026
29	NIGAH EXPANSION OCP (15 TO 25 MTPA) - [N06000196]	11/2020	1,729.68 -	1,729.68	-	03/2025 -	03/2025
30	BLOCK-B EXPANSION OPENCAST PROJECT - [N06000184]	7/2019	998.71 -	998.71	-	03/2023 -	03/2023
31	BINA KAKRI AMALGAMATION OCP 14 MTPA - [N06000192]	8/2020	836.42 -	836.42	60.07	03/2024 -	03/2024
	<u>South-Eastern Coal Fields Limited</u>						
32	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	9.09	03/2023 -	03/2023
33	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
34	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	100.63	03/2021 04/2024	04/2024
35	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
36	DIPKA OC EXPANSION 40 MTY - [N06000200]	12/2020	5,241.40 -	5,241.40	1,931.58	03/2029 -	03/2029

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
37	PORDA CHINTAPANI OCP (10 MTY) - [N06000199]	12/2020	2,310.12 -	2,310.12	-	03/2029 -	03/2029
38	JAMPALI OCP RCE - [N06000198]	5/2020	278.64 -	278.64	183.02	03/2024 -	03/2024
39	BAROUD OC EXPANSION (3-10 MTY) - [N06000197]	8/2020	2,309.80 -	2,309.80	275.61	03/2029 -	03/2029
40	JHIRIA WEST OPENCASST PROJECT - [N06000166]	11/2018	389.97 -	389.97	-	03/2026 -	03/2026
41	MAHAMAYA OPENCASST PROJECT - [N06000164]	5/2018	410.26 -	410.26	28.26	03/2026 -	03/2026
42	VIJAY WEST OPENCASST PROJECT - [N06000158]	5/2017	976.95 -	976.95	75.96	03/2026 -	03/2026
43	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	2,745.45	03/2023 -	03/2023
44	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	1.62	03/2022 -	03/2022
45	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	152.93	03/2022 -	03/2022
	<u>Western Coal Fields Limited</u>						
46	BHANEGAON OC - [N06000121]	2/2015	187.94 -	409.68	86.81	03/2023 -	03/2023
47	GANDHIGRAM UG MINE - [N06000183]	8/2019	414.16 -	414.16	.87	03/2026 -	03/2026
48	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	745.03	365.38	03/2025 -	03/2025
49	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	404.45	246.02	03/2022 -	03/2022
50	VISHNUPURI UG TO OC MINE - [N06000178]	7/2018	195.57 -	195.57	2.94	03/2025 -	03/2025
	Total		89,255.81 -	82,573.75	24,908.47		
	<u>FINANCE</u>						
	<u>Central Public Works Department</u>						
51	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]	11/2017	348.77 -	348.77	123.99	11/2021 -	11/2021
	Total		348.77 -	348.77	123.99		
	<u>HEALTH AND FAMILY WELFARE</u>						
52	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR [N21000029]	3/2019	1,404.00 -	1,404.00	200.58	09/2023 -	09/2023
53	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]	3/2019	1,577.00 -	1,828.00	-	09/2025 -	09/2025

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>National Building Construcion Corporation Ltd</u>						
54	AIIMS BILASPUR - [N21000028]	4/2018	1,351.00 -	1,471.00	712.04	09/2021 -	09/2021
	Total		4,332.00 -	4,703.00	912.62		
	<u>HOME AFFAIRS</u>						
	<u>Central Public Works Department</u>						
55	NSG AT KOLKATA - [N28000104]	10/2014	162.88 -	238.00	171.19	04/2018 12/2021	12/2021
56	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE- - [N28000147]	1/2020	166.98 167.00	166.98	-	10/2023 -	10/2023
57	BUILDING OF THE FORCE HEADQUARTER INCLUDING SECTOR HQR RAF - [N45000002]	6/2019	277.35 -	277.35	10.60	07/2022 -	07/2022
58	CONSTRUCTION OF SEPARATE FAMILY ACCOMMODATION (440 NOS.) (PHASE- C/O 336 NOS. TYPE- II QTRS , 96 - [N45000001]	1/2020	166.98 -	166.98	.29	05/2022 -	05/2022
	Total		774.19 -	849.31	182.08		
	<u>HUMAN RESOURCE DEVELOPMENT</u>						
59	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130]	3/2019	329.00 -	329.00	-	07/2022 -	07/2022
60	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR - [N42000008]	9/2018	392.51 -	392.51	38.44	06/2022 -	06/2022
61	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]	1/2018	676.00 -	676.00	-	04/2023 -	04/2023
62	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I. - [N28000141]	3/2020	808.62 -	808.62	57.42	07/2022 -	07/2022
	Total		2,206.13 -	2,206.13	95.86		
	<u>MINES</u>						
	<u>National Aluminum Company Limited (Nalco)</u>						
63	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	5,540.00 -	5,540.00	731.55	04/2021 12/2022	12/2022
64	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]	11/2017	483.00 -	483.00	.92	04/2021 03/2023	03/2023
	Total		6,023.00 -	6,023.00	732.47		

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	PETROLEUM						
	Bharat Petroleum Corporation Limited						
65	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]	11/2012	678.00 -	1,472.00	19.44	02/2017 08/2022	08/2022
66	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]	9/2018	11,130.00 -	11,130.00	379.09	03/2023 -	03/2023
67	MMPL PIPELINE REROUTING PROJECT - [N16000261]	4/2013	449.58 -	449.58	396.13	12/2019 04/2021	04/2021
68	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL - [N16000365]	12/2017	1,524.06 -	1,524.06	785.64	12/2021 -	12/2021
69	2ND GENERATION LIGNOCELLULOSIC BIOMASS ETHANOL BIOFUEL REFINERY AT BARGARH (ODISHA) - [N16000374]	8/2019	1,607.00 -	1,607.00	255.22	08/2022 -	08/2022
70	KEROSENE HYDROTREATER (KHT) UNIT INTEGRATED WITH EXISTING DIESEL HYDROTREATER (DHT) UNIT AT MUMBAI R - [N16000410]	8/2020	697.00 -	697.00	155.18	03/2023 -	03/2023
71	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY - [N16000397]	7/2020	640.00 -	640.00	326.57	12/2021 -	12/2021
72	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]	11/2018	248.55 -	248.55	109.38	06/2022 -	06/2022
	Gas Authority Of India Limited						
73	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	3/2017	1,933.00 -	1,933.00	1,268.75	12/2020 12/2021	12/2021
74	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]	6/2009	2,915.00 2,915.00	5,909.00	3,607.20	12/2012 02/2022	02/2022
75	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]	7/2017	243.53 -	243.53	115.28	07/2022 -	07/2022
76	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	345.15	200.77	04/2022 -	04/2022
77	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]	7/2017	182.20 -	182.20	78.03	07/2022 -	07/2022
78	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT - [N16000398]	6/2020	7,844.25 -	7,844.25	1,079.10	05/2023 -	05/2023
79	DHAMRA HALDIA PIPELINE PROJECT - [N16000391]	3/2020	1,030.65 -	1,030.65	53.10	11/2022 -	11/2022
80	CITY GAS DISTRIBUTION, JAMSHEDPUR - [N16000389]	10/2017	221.45 -	221.45	92.99	10/2022 -	10/2022
81	SRIKAKULAM ANGUL PIPELINE PROJECT - [N16000388]	9/2019	2,658.34 -	2,658.34	245.50	07/2022 -	07/2022
82	BARAUNI-GUWAHATI PIPELINE - [N16000334]	6/2018	3,308.00 -	3,060.00	2,272.30	12/2021 -	12/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
83	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329]	10/2017	226.45 -	226.45	110.99	10/2022 -	10/2022
84	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]	10/2017	359.25 -	359.25	143.73	10/2022 -	10/2022
85	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	3/2017	1,740.00 -	1,740.00	764.50	12/2020 12/2021	12/2021
86	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]	3/2017	3,437.00 -	3,048.00	1,852.90	12/2020 12/2021	12/2021
	<u>Hindustan Petroleum Corporation Limited</u>						
87	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,928.00 -	26,264.00	14,820.38	07/2020 07/2022	07/2022
88	BARMER PALANPUR PIPELINE - [N16000384]	11/2019	776.00 -	776.00	215.96	11/2022 -	11/2022
89	CITY GAS DISTRIBUTION IN UP AND UK - [N16000387]	3/2019	3,450.20 -	3,450.20	235.43	03/2029 08/2029	08/2029
90	SULPHUR FORMING UNIT IN SRU - [N16000408]	10/2020	210.94 -	210.94	117.03	08/2021 -	08/2021
91	RUF PITCH LOADING GANTRY - [N16000406]	10/2020	332.61 -	332.61	.01	11/2022 -	11/2022
92	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB [N16000402]	5/2020	1,421.46 -	1,244.50	76.19	02/2023 -	02/2023
93	CITY GAS DISTRIBUTION IN WEST BENGAL - [N16000392]	3/2019	5,830.20 -	5,830.20	93.97	03/2031 08/2029	08/2029
94	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS - [N16000385]	9/2018	520.00 -	520.00	126.72	09/2026 02/2027	02/2027
95	SETTING UP OF PHASE LL FACILITIES FOR HPCL GREEN R AND D CENTRE AT BENGALURU - [N16000380]	6/2018	380.00 -	380.00	222.20	11/2021 -	11/2021
96	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]	6/2017	161.50 -	161.50	78.18	06/2020 09/2021	09/2021
97	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	9/2017	2,677.00 -	3,072.00	2,239.96	06/2021 08/2022	08/2022
98	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE [N16000369]	12/2018	854.00 -	854.00	150.14	12/2022 -	12/2022
99	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367]	6/2019	2,166.38 -	2,166.38	922.06	06/2022 -	06/2022
100	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA [N16000312]	11/2017	255.00 -	300.00	271.70	11/2020 06/2021	06/2021
	<u>Indian Oil Corporation Limited</u>						
101	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	1,236.00	394.74	10/2017 03/2022	03/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
102	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA - [N16000386]	1/2020	14,810.00 -	14,810.00	934.70	04/2023 -	04/2023
103	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383]	9/2019	164.69 -	164.69	13.16	07/2021 03/2022	03/2022
104	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY - [N16000382]	11/2019	5,251.00 -	5,251.00	192.50	05/2023 -	05/2023
105	LPG BP PROJECT CHITTOOR - [N16000381]	7/2019	167.00 -	167.00	8.89	07/2022 -	07/2022
106	LAB REVAMP AT GUJARAT REFINERY - [N16000377]	10/2019	403.00 -	403.00	103.74	12/2021 -	12/2021
107	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]	8/2019	1,255.00 -	1,255.00	185.11	10/2021 -	10/2021
108	R and D CAMPUS II AT FARIDABAD - [N16000375]	6/2019	2,281.94 -	2,281.94	431.31	12/2022 07/2023	07/2023
109	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]	6/2019	371.00 -	371.00	4.44	09/2022 03/2023	03/2023
110	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT - [N16000363]	12/2018	278.60 -	278.60	44.73	06/2021 07/2022	07/2022
111	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]	5/2019	3,361.00 -	3,361.00	1,665.03	08/2021 09/2022	09/2022
112	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]	11/2018	462.30 -	462.30	23.19	09/2021 06/2022	06/2022
113	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]	10/2018	598.00 -	598.00	293.80	02/2020 02/2022	02/2022
114	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]	1/2019	909.00 -	909.00	309.94	01/2021 03/2022	03/2022
115	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP [N16000350]	10/2018	316.20 -	316.20	98.14	10/2021 03/2022	03/2022
116	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]	4/2018	522.00 -	522.00	323.87	03/2021 12/2021	12/2021
117	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]	8/2018	466.00 -	466.00	256.49	04/2021 12/2021	12/2021
118	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]	10/2017	906.00 -	906.00	279.82	02/2020 10/2021	10/2021
119	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]	12/2017	199.36 -	199.36	34.40	10/2020 08/2022	08/2022
120	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]	8/2017	255.40 -	255.40	64.34	08/2020 11/2021	11/2021
121	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY [N16000321]	4/2018	206.63 -	206.63	93.11	02/2020 08/2021	08/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
122	LPG BP PROJECT JODHPUR - [N16000318]	3/2018	229.80 -	229.80	81.48	- 05/2022	05/2022
123	LPG BP PROJECT MOTIHARI - [N16000317]	5/2018	206.50 -	206.50	134.97	03/2021 09/2021	09/2021
124	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU [N16000305]	12/2017	466.43 -	466.43	207.05	10/2020 01/2022	01/2022
125	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]	8/2017	236.00 -	293.00	161.05	06/2020 09/2021	09/2021
126	KHARAGPUR LPG BOTTLING PLANT - [N16000300]	4/2017	163.02 -	163.02	101.52	04/2020 10/2021	10/2021
127	AUGMENTATION OF CTMPL - [N16000286]	12/2016	228.00 -	228.00	140.61	11/2021 -	11/2021
128	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM [N16000411]	10/2020	1,614.00 -	1,614.00	-	08/2023 -	08/2023
129	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY [N16000409]	9/2020	18,936.00 -	18,936.00	715.09	09/2024 -	09/2024
130	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI [N16000403]	10/2020	921.00 -	921.00	19.14	09/2023 -	09/2023
131	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400]	6/2020	1,378.00 -	1,378.00	24.39	12/2022 -	12/2022
132	MUZAFFARPUR-MOTIHARI LPG PIPELINE - [N16000399]	6/2020	403.00 -	403.00	1.77	08/2022 -	08/2022
133	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY - [N16000396]	7/2020	13,805.00 -	13,805.00	92.75	01/2024 -	01/2024
134	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY - [N16000395]	1/2020	202.16 -	202.16	18.34	07/2022 -	07/2022
135	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY [N16000393]	6/2020	1,019.00 -	1,019.00	58.94	01/2023 -	01/2023
136	LPG BP PROJECT KHORDHA - [N16000283]	12/2016	161.59 -	161.59	49.59	12/2019 03/2022	03/2022
137	SITARGANJ LPG PROJECT - [N16000282]	2/2017	160.10 -	160.10	93.54	02/2020 06/2021	06/2021
138	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	5/2016	4,497.00 -	6,025.00	3,681.97	12/2018 02/2022	02/2022
139	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	1,536.61	02/2022 -	02/2022
140	PARADIP LPG IMPORT FACILITY - [N16000196]	1/2015	690.00 -	690.00	545.44	07/2018 05/2021	05/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
141	PARADIP HYDERABAD PIPELINE - [N16000194]	1/2015	2,321.00 -	3,338.00	2,923.70	12/2020 03/2022	03/2022
142	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	1/2015	1,823.00 -	3,027.90	1,957.55	03/2021 12/2021	12/2021
143	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR), CACHAR, ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]	6/2016	423.00 -	502.00	422.12	08/2019 06/2021	06/2021
144	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]	8/2018	1,636.00 -	1,636.00	723.59	08/2020 04/2022	04/2022
145	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]	8/2018	557.00 -	557.00	496.45	02/2020 06/2021	06/2021
146	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]	4/2018	5,654.00 -	5,654.00	2,826.29	10/2021 -	10/2021
147	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]	7/2018	189.00 -	189.00	149.34	01/2021 06/2021	06/2021
148	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT - [N16000336]	3/2018	588.20 -	730.20	77.30	- 05/2023	05/2023
149	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]	3/2018	676.00 -	676.00	433.41	08/2022 -	08/2022
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
150	DEVANGONTHI MARKETING TERMINAL - [N16000401]	6/2020	200.00 -	200.00	2.26	06/2023 -	06/2023
	<u>Numaligarh Refinery Limited</u>						
151	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY - [N16000379]	1/2019	12,366.00 -	12,366.00	168.82	10/2024 -	10/2024
152	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES - [N16000394]	1/2019	10,228.00 -	10,228.00	117.34	10/2024 -	10/2024
	<u>Oil & Natural Gas Corporation Limited</u>						
153	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	3/2011	861.79 -	2,001.00	1,551.48	05/2013 02/2022	02/2022
154	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]	2/2019	2,292.46 -	2,203.71	1,757.87	05/2021 12/2021	12/2021
155	REDEVELOPMENT OF NANDASAN FIELD - [N16000404]	2/2020	444.87 -	444.87	87.40	08/2022 -	08/2022
156	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]	5/2019	763.92 -	733.86	757.62	12/2020 05/2021	05/2021
157	HEERA REDEVELOPMENT - PHASE III - [N16000360]	6/2019	2,494.68 -	2,354.72	1,421.11	03/2022 -	03/2022
158	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]	5/2019	3,660.71 -	3,740.05	2,808.52	05/2021 01/2022	01/2022
159	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]	4/2019	3,228.80 -	3,976.67	1,188.33	03/2022 05/2023	05/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
160	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	823.27 -	1,137.79	669.73	03/2023 03/2022	03/2022
161	Field Development Plan of Madanam NELP-IV Block CY- ONN-2002 - [N16000241]	11/2015	650.82 -	624.35	447.05	03/2019 09/2021	09/2021
162	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	7/2016	249.85 250.00	303.75	199.31	05/2020 05/2021	05/2021
163	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]	2/2017	4,006.83 -	3,596.00	3,514.02	05/2021 05/2021	05/2021
164	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	970.30	832.63	03/2026 -	03/2026
165	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]	3/2016	34,012.00 -	25,090.00	11,254.33	06/2020 06/2022	06/2022
166	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,375.90	2,786.78	04/2018 05/2022	05/2022
	Total		2,58,881.32 -	2,65,055.58	86,875.77		
	<u>POWER</u>						
	<u>National Hydro-Electric Power Corporation</u>						
167	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	9/2002	3,919.59 -	9,897.59	8,945.10	09/2009 07/2022	07/2022
168	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	9/2003	6,285.33 -	19,992.43	13,732.39	09/2010 08/2023	08/2023
	<u>National Thermal Power Corporation</u>						
169	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	13,140.91	11,730.23	12/2018 05/2021	05/2021
170	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58 -	15,389.42	11,722.10	06/2019 10/2022	10/2022
171	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.54	668.04	09/2019 12/2024	12/2024
172	DEVIKOT SOLAR 150MW - [N18000281]	1/2020	798.24 -	798.24	34.64	09/2021 01/2022	01/2022
173	KAWAS SOLAR 56 MW - [N18000283]	8/2020	261.80 -	261.80	-	10/2021 -	10/2021
174	SAMBHU KI BHURJ SOLAR 250 MW - [N18000285]	1/2020	1,522.71 -	1,522.71	437.60	09/2021 01/2022	01/2022
175	KAYAMKULAM SOLAR 70 MW - [N18000288]	9/2019	403.62 -	403.62	53.13	06/2021 10/2021	10/2021
176	ETTAYAPURAM SOLAR 230MW - [N18000290]	3/2020	1,316.22 -	1,316.22	-	09/2021 -	09/2021
177	FATEHGARH SOLAR 296MW - [N18000289]	3/2020	1,749.31 -	1,749.31	-	09/2021 -	09/2021
178	SAMBHU KI BHURJ-II SOLAR 300MW - [N18000286]	3/2020	1,782.00 -	1,782.00	200.75	09/2021 01/2022	01/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
179	RAMAGUNDAM FLOATING SOLAR 100 MW - [N18000284]	6/2019	401.90 -	401.90	-	04/2021 -	04/2021
180	NOKHRA - [N18000282]	3/2020	1,722.14 -	1,722.14	132.85	09/2021 01/2022	01/2022
181	DEVIKOT SOLAR 90MW - [N18000280]	3/2020	501.29 -	501.29	118.11	09/2021 01/2022	01/2022
182	BARH STPP(3X660MW) NTPC - [180100242]	2/2005	8,692.97 -	21,312.11	18,595.56	10/2011 07/2023	07/2023
183	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	1/2016	10,598.98 -	10,997.70	8,368.64	11/2020 07/2022	07/2022
	<u>Power Grid Corporation Of India Limited</u>						
184	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	2/2009	11,130.19 -	14,719.10	12,894.95	08/2013 08/2022	08/2022
185	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]	2/2017	5,070.13 -	5,070.13	4,101.57	04/2020 06/2021	06/2021
186	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]	11/2017	358.83 -	358.83	253.49	05/2020 05/2021	05/2021
187	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]	8/2017	1,931.39 -	1,931.39	1,709.25	02/2020 06/2021	06/2021
188	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]	3/2015	1,394.52 -	1,394.52	534.89	05/2017 09/2021	09/2021
	<u>Satluj Jal Vidyut Nigam Limited</u>						
189	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]	3/2019	10,439.09 -	10,439.09	2,035.50	01/2024 -	01/2024
190	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	947.89	577.17	12/2021 -	12/2021
191	LUHRI HYDROELECTRIC PROJECT (STAGE1) - [N18000279]	11/2020	1,810.56 -	1,810.56	422.46	01/2026 -	01/2026
	<u>Thdc India Limited</u>						
192	AMELIA COAL MINE - [N18000252]	1/2017	2,104.21 -	1,587.16	495.58	09/2020 08/2022	08/2022
	Total		1,03,124.21 -	1,40,829.60	97,764.00		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
193	WARDHA-NANDED MAHARASHTRA - [N22000231]	4/2008	3,168.29 -	3,168.29	1,352.27	03/2023 -	03/2023
194	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	2/2016	2,750.00 -	3,438.51	-	03/2024 -	03/2024
195	DAUND - MANMAD (236 KM) - [N22000360]	2/2016	1,876.00 -	2,081.27	445.15	03/2023 -	03/2023
196	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]	2/2016	9,968.00 -	9,968.00	-	03/2024 -	03/2024

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
197	PUNE-NASIK (265 KM) - [N22000354] <u>East Coast Railway</u>	2/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024
198	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	4/2005	810.78 -	1,928.07	873.81	06/2021 03/2025	03/2025
199	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]	4/2015	1,172.92 -	1,172.92	613.52	12/2018 03/2024	03/2024
200	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]	4/2015	2,361.74 -	2,361.74	432.17	03/2022 03/2026	03/2026
201	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]	4/2015	2,499.71 -	2,499.71	671.08	03/2022 03/2024	03/2024
202	JAGDALPUR-KORAPUT DOUBLING - [N22000376]	4/2015	1,547.38 -	1,547.38	612.77	03/2022 03/2023	03/2023
203	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	4/1994	2,923.13 -	3,791.66	1,506.95	03/2009 03/2026	03/2026
204	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,160.83	950.18	03/2020 03/2023	03/2023
205	BHADRAK - NERGUNDI 3RD LINE - [N22000316] <u>North Central Railway</u>	3/2013	843.04 -	843.04	227.52	10/2020 03/2024	03/2024
206	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495] <u>North Eastern Railway</u>	3/2018	4,329.53 -	4,329.53	33.37	03/2023 -	03/2023
207	HATHUA-BHATNI (N L) (NER) - [220100319]	4/2005	230.03 -	230.03	277.14	12/2022 -	12/2022
208	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,295.42 -	1,295.42	1,111.50	03/2022 -	03/2022
209	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131] <u>Northern Railway</u>	3/2007	243.78 -	895.00	111.89	12/2021 -	12/2021
210	CHANDIGARH-BADDI - [N22000467] <u>National High Speed Rail Corporation Limited</u>	4/2007	328.14 -	1,540.13	242.04	03/2023 03/2025	03/2025
211	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463] <u>Rail Vikas Nigam Ltd.</u>	12/2015	1,08,000.00 -	1,08,000.00	12,039.69	12/2023 -	12/2023
212	AHMEDABAD-BOTAD (GC) - [N22000140]	4/2012	975.62 -	1,500.00	1,497.74	12/2021 -	12/2021
213	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	773.94 -	850.00	705.50	12/2024 -	12/2024
214	VIJAYAWADA-GUDUR - [N22000369]	4/2015	3,246.26 -	3,548.68	2,224.17	12/2023 -	12/2023
215	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501] <u>South Western Railway</u>	6/2016	3,677.76 -	3,677.76	446.65	12/2023 -	12/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
216	HUBLI- CHIKAJAJUR - [N22000325]	3/2015	1,156.94 -	1,656.00	1,160.49	03/2020 03/2023	03/2023
217	HOTGI-KUDGI-GADAG - [N22000333]	3/2015	1,614.59 -	1,870.41	1,341.15	03/2019 03/2024	03/2024
218	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	3/1996	644.78 -	998.00	463.45	03/2017 03/2025	03/2025
219	ARSIKERE-TUMKUR - [N22000332]	3/2015	578.00 -	783.00	620.29	03/2020 06/2021	06/2021
	<u>Southern Railway</u>						
220	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	4/2007	931.98 -	1,121.00	928.75	- 05/2021	05/2021
	<u>Western Railway</u>						
221	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	4/2008	3,503.69 -	5,912.40	2,161.74	03/2022 03/2024	03/2024
222	CHOTTAUDEPUR-DHAR(NL) - [N22000138]	4/2007	1,347.26 -	1,347.26	907.54	03/2022 03/2023	03/2023
223	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]	4/2011	844.10 -	844.10	186.59	- 03/2024	03/2024
224	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]	2/1991	551.51 -	890.76	745.11	03/2019 10/2021	10/2021
225	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]	4/2016	700.00 -	603.69	254.73	06/2020 03/2023	03/2023
226	SURENDRA NAGAR RAJKOT - [N22000392]	4/2015	1,002.39 -	1,002.39	653.86	03/2021 12/2022	12/2022
227	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	4/2011	1,037.15 -	1,389.05	1,125.73	03/2021 12/2021	12/2021
228	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	4/1994	320.66 -	1,378.11	540.09	03/2019 03/2023	03/2023
229	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]	4/2007	1,640.04 -	1,640.04	866.42	03/2022 03/2023	03/2023
230	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	4/2008	829.74 -	1,959.74	1,799.00	03/2020 03/2024	03/2024
231	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	4/2008	318.24 -	411.62	126.05	03/2012 03/2023	03/2023
	Total		1,73,627.54 -	1,88,977.22	40,256.10		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
232	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]	12/2015	291.05 -	291.05	212.46	- 06/2021	06/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
233	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 - [N24001229	12/2014	379.16 -	379.16	272.43	11/2017 06/2021	06/2021
234	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228	11/2017	188.80 -	188.80	78.69	05/2019 06/2021	06/2021
235	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226	12/2014	496.02 -	496.02	240.11	03/2015 06/2021	06/2021
236	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222	3/2016	452.94 -	435.61	94.34	07/2016 06/2021	06/2021
237	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221	1/2016	624.98 -	731.50	416.16	10/2016 06/2021	06/2021
238	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219	1/2016	476.20 544.00	544.00	400.38	09/2016 06/2021	06/2021
239	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218	11/2015	335.32 -	335.32	269.15	06/2017 06/2021	06/2021
240	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963	1/2018	418.03 -	418.03	194.62	08/2018 05/2021	05/2021
241	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933	2/2017	429.43 -	429.43	256.15	11/2017 04/2021	04/2021
242	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931	11/2016	290.15 -	290.15	73.11	05/2017 07/2021	07/2021
243	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929	9/2016	372.68 -	372.68	185.04	02/2017 06/2021	06/2021
244	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899	3/2016	877.79 -	877.79	687.99	06/2019 04/2021	04/2021
245	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898	1/2016	809.16 -	809.16	573.85	07/2018 05/2021	05/2021
246	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896	1/2017	373.82 -	373.82	197.04	09/2019 06/2021	06/2021
247	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890	3/2018	217.22 -	226.88	170.96	08/2018 09/2021	09/2021
248	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881	11/2017	184.62 -	184.62	86.32	02/2018 06/2021	06/2021
249	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217	1/2016	497.14 -	572.66	270.56	08/2016 06/2021	06/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
250	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I - [N24001216	12/2016	196.00 -	196.00	47.95	09/2021 -	09/2021
251	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198	1/2019	264.50 -	264.50	85.70	03/2021 11/2021	11/2021
252	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197	3/2018	351.00 -	351.00	128.70	06/2021 -	06/2021
253	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180	3/2019	237.51 -	237.51	60.04	12/2022 -	12/2022
254	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152	9/2018	160.00 -	160.00	101.70	09/2021 -	09/2021
255	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151	11/2017	392.33 -	428.55	351.92	03/2018 06/2021	06/2021
256	BHOGAN KHURD TO KASHEDI - [N24001132	9/2017	743.21 743.00	743.21	193.08	06/2021 -	06/2021
257	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091	3/2016	536.65 356.00	536.65	539.35	12/2019 06/2021	06/2021
258	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307	1/2017	197.67 -	197.67	5.75	12/2022 -	12/2022
259	NAGAU-BIKANER SECTION FROM KM 177.00 TO KM 267.325 ON NH-89 - [N24001240	3/2020	370.36 -	370.36	90.45	08/2022 -	08/2022
260	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513	3/2015	511.83 -	511.83	375.50	08/2017 06/2021	06/2021
261	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478	12/2015	957.54 -	957.54	756.69	02/2020 04/2021	04/2021
262	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312	4/2013	151.59 -	370.01	281.74	08/2013 06/2021	06/2021
263	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313	4/2013	166.27 -	359.92	243.59	08/2013 06/2021	06/2021
264	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314	1/2013	182.28 -	369.64	274.07	02/2013 06/2021	06/2021
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
265	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68. - [N24001244	8/2020	301.06 -	301.06	-	04/2022 -	04/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
266	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923 - [N24001250	8/2020	278.46 -	278.46	12.06	03/2022 -	03/2022
267	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM - [N24001259	9/2020	315.63 -	315.63	-	04/2022 -	04/2022
268	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM32.0 TO KM43.454 [DES - [N24001258	8/2020	202.36 -	202.36	-	04/2022 -	04/2022
269	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG - [N24001257	8/2020	159.85 -	159.85	-	10/2022 -	10/2022
270	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D - [N24001255	9/2020	277.44 -	277.44	-	10/2022 -	10/2022
271	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D - [N24001256	8/2020	6,808.69 -	6,808.69	-	09/2026 -	09/2026
272	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 - [N24001254	3/2020	242.97 -	242.97	-	06/2022 -	06/2022
273	CONSTRUCTION, OPERATION AND MAINTENANCE OF Z-MORH TUNNEL INCLUDING APPROACHES ON NH-01 SRINAGAR-SONA - [N24001253	12/2019	2,680.42 -	2,680.42	-	12/2023 -	12/2023
274	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 - [N24001252	8/2020	295.97 -	295.97	-	04/2023 -	04/2023
275	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N - [N24001251	3/2019	402.94 -	402.94	-	04/2022 -	04/2022
276	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137 - [N24001268	3/2019	471.00 -	471.00	-	07/2022 -	07/2022
277	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID - [N24001267	3/2020	178.43 -	178.43	-	07/2022 -	07/2022
278	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K - [N24001266	7/2020	210.79 -	210.79	-	04/2022 -	04/2022
279	REHABILITATION & UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE SE - [N24001265	3/2020	154.51 -	154.51	-	07/2022 -	07/2022
280	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL - [N24001264	7/2020	228.39 -	228.39	-	04/2022 -	04/2022
281	REHABILITATION & UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION - [N24001263	6/2020	277.50 -	277.50	-	01/2022 -	01/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
282	CONSTRUCTION & UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT - [N24001262]	7/2020	345.38	345.38	-	04/2023	04/2023
283	CONSTRUCTION & UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT - [N24001261]	8/2020	311.00	311.00	-	04/2023	04/2023
284	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 TO - [N24001260]	9/2020	257.15	257.15	17.77	04/2022	04/2022
285	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D] - [N24001288]	8/2020	232.29	232.29	-	04/2022	04/2022
286	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) - [N24001287]	4/2020	330.80	330.80	11.57	12/2021	12/2021
287	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV) - [N24001285]	3/2020	330.78	330.78	23.74	12/2021	12/2021
288	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) - [N24001286]	3/2020	278.95	278.95	56.76	06/2022	06/2022
289	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III) - [N24001284]	3/2020	361.53	361.53	13.17	06/2022	06/2022
290	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV) - [N24001283]	3/2020	281.78	281.78	38.40	07/2022	07/2022
291	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) - [N24001282]	3/2020	355.79	355.79	31.76	06/2022	06/2022
292	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) - [N24001281]	3/2020	292.24	292.24	29.00	07/2022	07/2022
293	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I) - [N24001280]	3/2020	320.97	320.97	18.73	06/2022	06/2022
294	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II) - [N24001279]	3/2020	216.49	216.49	28.93	07/2022	07/2022
295	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) - [N24001278]	3/2020	206.88	206.88	9.33	07/2022	07/2022
296	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54 - [N24001277]	9/2020	275.02	275.02	14.15	10/2022	10/2022
297	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI - [N24001276]	8/2020	228.97	228.97	-	04/2022	04/2022
298	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO - [N24001275]	8/2020	268.98	268.98	-	04/2022	04/2022
299	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI - [N24001274]	8/2020	379.39	379.39	-	04/2022	04/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
300	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) - [N24001273	7/2020	177.76 -	177.76	.64	08/2022 -	08/2022
301	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) - [N24001272	3/2020	167.95 -	167.95	1.12	06/2022 -	06/2022
302	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) - [N24001271	6/2020	365.53 -	365.53	3.35	08/2022 -	08/2022
303	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) - [N24001270	3/2020	292.24 -	292.24	1.74	06/2022 -	06/2022
304	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 1B) - [N24001269	3/2020	216.49 -	216.49	3.35	03/2022 -	03/2022
305	2-LANING FROM MANU-SIMLUNG (PKG III) - [N24001249	6/2020	347.36 -	347.36	-	01/2022 -	01/2022
306	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO - [N24001245	9/2020	353.90 -	353.90	4.21	05/2022 -	05/2022
307	4-LANING OF HAPACHARA - TULUNGIA SECTION - [N24001246	3/2020	220.20 -	220.20	-	12/2022 -	12/2022
308	2-LANING FROM MANU-SIMLUNG (PKG I) - [N24001247	3/2020	247.76 -	247.76	2.60	01/2022 -	01/2022
309	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800 - [N24001248	8/2020	208.84 -	208.84	-	04/2022 -	04/2022
	<u>National Highways Authority Of India</u>						
310	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435	10/2015	531.13 -	730.97	653.06	05/2018 06/2021	06/2021
311	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664	3/2017	639.79 -	552.90	597.77	03/2020 05/2021	05/2021
312	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441	10/2015	593.26 -	690.17	595.33	05/2018 06/2021	06/2021
313	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN - [N24001306	10/2020	724.60 -	724.60	-	03/2023 -	03/2023
314	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA - [N24001302	7/2020	3,426.00 -	3,426.00	-	12/2021 -	12/2021
315	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552	3/2016	701.40 -	701.40	132.05	03/2019 03/2022	03/2022
	Total		41,108.26 -	42,195.94	10,516.18		
	<u>RURAL DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
316	CONSTRUCTION OF GRAMEEN VIKAS BHAWAN (2BASEMENTS+ GROUND+9 FLOORS) FOR MINISTRY OF RURAL DEVELOPMENT - [N28000132	11/2018	361.60 -	361.60	12.44	07/2021 -	07/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		361.60 -	361.60	12.44		
	<u>SHIPPING AND PORTS</u>						
	<u>Inland Waterways Authority Of India</u>						
317	JAL MARG VIKAS PROJECT - [N25000072]	1/2018	5,369.18 -	4,633.81	1,871.35	03/2023 -	03/2023
	Total		5,369.18 -	4,633.81	1,871.35		
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
318	NMDC INTEGRATED STEEL PLANT - [N12000086]	1/2010	15,525.00 -	21,940.00	18,516.49	05/2015 07/2021	07/2021
319	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 - [N12000124]	11/2015	2,907.00 -	2,907.00	256.24	06/2023 -	06/2023
	<u>Rastriya Ispat Nigam Limited</u>						
320	FORGED WHEEL PLANT - [N12000116]	4/2014	1,682.85 -	1,682.85	1,564.62	09/2018 06/2021	06/2021
321	COKE OVEN BATTERY-5 - [N12000117]	12/2011	2,858.00 -	2,558.00	1,838.96	12/2017 12/2021	12/2021
	<u>Steel Authority Of India Limited (Sail)</u>						
322	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]	3/2015	1,034.01 -	1,034.01	537.82	10/2017 12/2021	12/2021
323	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY - [N12000122]	11/2020	377.18 -	377.18	32.76	05/2023 -	05/2023
324	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP - [N12000123]	11/2020	542.24 -	542.24	31.68	12/2023 -	12/2023
	Total		24,926.28 -	31,041.28	22,778.57		
	<u>URBAN DEVELOPMENT</u>						
	<u>Ahmedabad Metro Rail</u>						
325	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137]	3/2019	5,384.17 -	5,384.17	63.77	03/2024 -	03/2024
326	SURAT METRO RAIL PROJECT - [N28000138]	3/2019	12,020.32 -	12,020.32	20.65	03/2024 -	03/2024
	<u>Central Public Works Department</u>						
327	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]	10/2016	422.00 -	422.00	70.75	03/2021 07/2021	07/2021
328	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]	10/2016	1,128.00 -	1,128.00	22.00	03/2022 -	03/2022
	<u>Delhi Metro Rail Corporation</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
329	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS - [N28000135]	7/2019	24,948.65 -	24,948.65	1,763.02	03/2025 -	03/2025
	<u>Lucknow Metro Rail Corporation Limited</u>						
330	KANPUR METRO RAIL PROJECT - [N28000144]	5/2019	11,076.48 -	11,076.48	-	03/2024 -	03/2024
331	AGRA METRO RAIL PROJECT - [N28000145]	5/2019	8,379.62 -	8,379.62	-	03/2024 -	03/2024
	<u>Maharashtra Metro Rail Corporation Ltd.</u>						
332	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]	12/2016	11,420.00 -	11,420.00	6,214.58	11/2021 -	11/2021
	<u>Madhya Pradesh Metro Rail Co Limited</u>						
333	BHOPAL METRO RAIL - [N28000124]	11/2018	6,941.40 -	6,941.40	174.53	02/2023 -	02/2023
334	INDORE METRO RAIL - [N28000125]	11/2018	7,500.80 -	7,500.80	130.21	02/2023 -	02/2023
	<u>National Capital Region Transport Corp</u>						
335	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134]	3/2019	30,274.00 -	30,274.00	3,416.31	06/2025 -	06/2025
	<u>Patna Metro Rail Corporation</u>						
336	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]	2/2019	13,365.77 -	13,365.77	231.97	06/2024 -	06/2024
	Total		1,32,861.21 -	1,32,861.21	12,107.79		
	<u>WATER RESOURCES</u>						
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>						
337	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026]	3/2018	230.06 -	230.06	73.63	07/2021 -	07/2021
338	SEWER NETWORKS, SPS AND STP, MUNGER - [N30000036]	3/2018	294.02 -	294.02	-	10/2021 -	10/2021
339	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA - [N30000051]	8/2017	824.00 -	824.00	40.09	06/2022 -	06/2022
340	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]	8/2017	578.89 -	578.89	40.09	06/2022 -	06/2022
341	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]	3/2017	277.42 -	277.42	146.23	05/2021 -	05/2021
342	SEWERAGE SCHEME AT PAHARI ZONE IVA S PATNA - [N30000041]	5/2017	184.86 -	184.86	152.78	05/2021 -	05/2021
343	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]	5/2017	356.37 -	356.37	93.34	04/2021 -	04/2021
	<u>Delhi Jal Board</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
344	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014]	3/2017	665.78 -	665.78	194.55	12/2022 -	12/2022
	<u>Kolkata Metropolitan Development Authority</u>						
345	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]	1/2019	384.96 -	384.96	-	04/2022 -	04/2022
346	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]	8/2017	185.22 -	185.22	-	12/2021 -	12/2021
347	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048]	1/2018	172.10 -	172.10	-	12/2021 -	12/2021
348	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]	10/2017	164.93 -	164.93	-	12/2021 -	12/2021
349	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046]	2/2014	274.76 -	274.76	202.13	12/2019 05/2021	05/2021
350	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]	12/2018	234.31 -	234.31	-	04/2022 -	04/2022
351	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033]	3/2018	165.16 -	165.16	-	06/2022 -	06/2022
352	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA - [N30000034]	8/2017	307.12 -	307.12	-	09/2022 -	09/2022
353	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPURL - [N30000030]	3/2019	287.53 -	287.53	-	04/2022 -	04/2022
	<u>Uttar Pradesh Jal Nigam</u>						
354	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006]	5/2017	767.59 -	767.59	76.71	09/2021 -	09/2021
355	INTEGRATED PROJECT FOR DEVELOPMENT OF STPS IN ALLAHABAD ALONG WITH EXISTING ASSETS - [N30000007]	3/2018	904.00 -	904.00	136.55	09/2021 -	09/2021
356	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]	2/2019	681.78 -	690.71	-	06/2022 -	06/2022
357	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022]	1/2019	206.05 -	206.05	29.26	10/2021 -	10/2021
358	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]	1/2019	231.79 -	234.03	-	12/2021 -	12/2021
359	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]	10/2017	213.62 -	261.12	-	03/2022 -	03/2022
360	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010]	3/2018	967.23 -	967.23	40.59	09/2021 -	09/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
361	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH [N30000013]	3/2019	271.39 -	271.39	-	08/2021 -	08/2021
	Total		9,830.94 -	9,889.61	1,225.95		
	Grand Total		8,58,212.22	9,17,955.65	3,01,480.46		

List of Projects Ahead of Schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>FERTILISERS</u>						
	<u>National Fertiliser Limited</u>						
1	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014	1/2018	215.92 -	215.92	168.30	11/2019 06/2021	05/2021
2	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015	1/2018	218.83 -	218.83	191.30	11/2019 05/2021	04/2021
3	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016	1/2018	239.81 -	239.81	199.11	11/2019 05/2021	04/2021
	Total		674.56 -	674.56	558.71		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Central Public Works Department</u>						
4	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150	3/2019	1,828.00	1,828.00	-	09/2025 -	05/2024
	Total		1,828.00 -	1,828.00	.00		
	<u>PETROLEUM</u>						
	<u>Gas Authority Of India Limited</u>						
5	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273	3/2017	2,433.00 -	2,433.00	2,110.70	12/2020 12/2021	06/2021
	<u>Hindustan Petroleum Corporation Limited</u>						
6	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315	6/2017	249.26 -	249.26	134.44	06/2020 12/2021	09/2021
	<u>Indian Oil Corporation Limited</u>						
7	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308	8/2017	315.00 -	315.00	208.09	12/2021 -	08/2021
8	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI - [N16000405	10/2020	1,398.00 -	1,398.00	80.68	12/2023 -	05/2023
9	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332	3/2018	3,712.00 -	3,696.00	1,995.95	09/2022 -	03/2022
	Total		8,107.26 -	8,091.26	4,529.86		
	<u>POWER</u>						

Costing Rs. 150 Crore and above

(April 2021)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Power Grid Corporation Of India Limited</u>						
10	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 546.36	546.36	478.29	11/2016 09/2021	06/2021
11	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]	2/2017	235.53 -	235.53	151.12	06/2019 08/2021	06/2021
	Total		757.82 -	781.89	629.41		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
12	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	2/2015	3,627.47	3,627.47	1,204.21	03/2024 -	03/2023
	<u>Metropolitan Rapid Transport Projects</u>						
13	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	4/2006	495.74	734.01	510.69	06/2013 06/2022	12/2021
	<u>North East Frontier Railway</u>						
14	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) [N22000390]	4/2016	602.27 -	2,144.78	921.83	12/2021 -	04/2021
	<u>Rail Vikas Nigam Ltd.</u>						
15	BHANUPALI-BILASPUR BERI NL - [N22000273]	4/2008	2,966.99 -	6,753.42	926.84	12/2026 -	12/2025
16	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78 -	723.78	0.19	12/2025 -	03/2025
17	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	4/2010	2,127.00 -	3,000.00	2,208.46	03/2023 -	12/2022
	<u>South Central Railway</u>						
18	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	4/2010	704.31 -	927.94	534.34	03/2020 03/2022	06/2021
	<u>Southern Railway</u>						
19	MADURAI-BODINAYAKKANUR - [N22000201]	4/2008	164.41	608.13	375.67	- 10/2021	09/2021
	<u>West Central Railway</u>						
20	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314]	4/2001	424.60	2,909.99	1,229.79	03/2021 03/2029	03/2023
	Total		11,836.57 -	21,429.52	7,912.02		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>National Highways Authority Of India</u>						
21	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]	11/2016	1,064.88 -	1,021.00	336.32	- 01/2022	07/2021
22	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]	3/2018	1,532.62 -	2,499.00	761.73	03/2021 10/2021	04/2021
	Total		2,597.50 -	3,520.00	1,098.05		

Costing Rs. 150 Crore and above

(April 2021)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>WATER RESOURCES</u>						
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>						
23	I AND D AND STP AT CHAPPRA - [N30000028	11/2018	236.15 -	236.15	46.50	12/2020 06/2021	04/2021
	Total		236.15 -	236.15	46.50		
	Grand Total		26,037.86	36,561.38	14,774.55		

List of projects without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2021)	
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>COAL</u>				
	<u>Bharat Coking Coal Limited</u>				
1	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	04/2014 -	04/2020
2	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND	02/2014	555.52 -	03/2021 -	-
	<u>Eastern Coal Fields Limited</u>				
3	RANIGANJ MASTER PLAN - [N06000163]ECL, WEST BENGAL	08/2009	2,661.73 -	08/2019 -	-
	<u>Mahanadi Coal Fields Limited</u>				
4	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	03/2012 -	03/2021
	<u>Neyveli Lignite Corporation</u>				
5	TALABIRA II AND III OCP - [N06000189]NLC,ODISHA	07/2017	2,401.07 -	07/2020 -	04/2020
6	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 7,980.79	12/2015 -	02/2021
7	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN	03/2015	522.45 -	09/2019 -	-
8	BARSINGSAR THERMAL POWER STATION EXTENSION - [N06000187]NLC,RAJASTHAN	03/2015	2,112.60 -	09/2020 -	-
9	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188]NLC,RAJASTHAN	03/2015	2,196.30 -	09/2020 -	-
10	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN	03/2015	513.63 -	12/2019 -	-
	<u>Singareni Colliers Company Limited</u>				
11	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 -	03/2016 -	03/2021
	<u>South-Eastern Coal Fields Limited</u>				
12	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	03/2014 -	03/2021
	<u>Western Coal Fields Limited</u>				
13	AMALGAMATED PAUNI-II III OC MINE - [N06000131]WCL,MAHARASHTRA	06/2015	483.69 499.00	03/2021 -	03/2021
	Total		18,583.15 -		
	<u>MINES</u>				
	<u>National Aluminum Company Limited (Nalco)</u>				
14	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]NALCO,TAMIL NADU	09/2017	166.62 163.17	06/2019 06/2021	12/2020

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
15	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]NALCO,ODISHA	12/2015	355.00 -	11/2020 -	02/2021
16	UTKAL D AND E COAL BLOCK - [N10000011]NALCO,ODISHA	05/2016	534.00 -	01/2020 -	-
	Total		1,055.62 -		
	<u>PETROLEUM</u>				
	<u>Bharat Petroleum Corporation Limited</u>				
17	PUNE POL STORAGE DEPOT - [N16000313]BPCL,MAHARASHTRA	08/2016	282.64 -	08/2020 -	03/2021
	<u>Chennai Petroleum Corporation Limited</u>				
18	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU	09/2017	1,858.00 -	12/2019 -	-
	<u>Hindustan Petroleum Corporation Limited</u>				
19	220 KV GRID SUPPLY - [N16000407]HPCL,ANDHRA PRADESH	10/2020	303.40 -	03/2021 -	-
20	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL,MAHARASHTRA	09/2015	4,199.00 5,060.00	03/2020 -	-
	<u>Indian Oil Corporation Limited</u>				
21	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]IOCL,ANDHRA PRADESH	08/2017	384.58 -	04/2021 03/2021	03/2021
22	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	06/2020 -	-
	<u>Oil India Limited</u>				
23	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	03/2017 -	03/2021
	Total		8,091.18 -		
	<u>POWER</u>				
	<u>National Hydro-Electric Power Corporation</u>				
24	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR	12/1999	578.62 -	06/2006 -	-
	<u>National Thermal Power Corporation</u>				
25	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	02/2017 -	01/2021
26	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000273]NTPC,UTTAR PRADESH	12/2018	587.44 -	09/2020 -	01/2021
27	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	03/2013	11,638.55 -	01/2018 -	02/2021
28	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH	09/2014	9,188.98 -	07/2019 03/2021	03/2021
29	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	09/2016 -	-

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
30	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC, CHHATISGARH	12/2012	11,846.00 -	10/2017 -	-
31	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC, UTTARAKHAND	07/2012	1,527.00 -	08/2017 -	-
32	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC, MADHYA PRADESH	03/2015	9,870.51 -	01/2020 -	-
33	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC, JHARKHAND	10/2004	4,237.96 4,238.00	10/2017 -	-
34	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC, CHHATISGARH	09/2015	3,004.00 -	11/2019 -	-
35	JETSAR SOLAR 160 MW - [N18000287]NTPC, RAJASTHAN	12/2019	702.28 -	03/2021 -	-
	<u>North East Electric Power Corporation</u>				
36	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO, ARUNACHAL PRADESH	12/2004	2,496.90 7,927.34	12/2009 02/2021	-
	<u>Power Grid Corporation Of India Limited</u>				
37	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL, MULTI STATE	10/2016	408.46 516.12	01/2019 09/2020	04/2020
38	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL, MULTI STATE	09/2017	198.49 -	09/2019 09/2020	05/2020
39	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL, MULTI STATE	10/2013	1,364.52 1,891.41	04/2016 09/2020	07/2020
40	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL, GUJARAT	05/2017	175.64 -	09/2018 11/2020	09/2020
41	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL, GUJARAT	12/2017	193.14 -	06/2019 11/2020	09/2020
42	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL, MULTI STATE	01/2015	871.62 902.49	10/2017 05/2021	01/2021
43	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL, KARNATAKA	05/2017	445.89 675.73	02/2019 02/2021	02/2021
44	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL, MULTI STATE	10/2008	4,824.12 5,071.94	10/2012 11/2020	03/2021
45	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL, MULTI STATE	10/2011	487.49 -	06/2014 -	-
46	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL, MULTI STATE	06/2014	5,151.37 -	03/2018 -	-
47	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL, MULTI STATE	01/2015	203.28 -	07/2017 -	-
48	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL, MULTI STATE	05/2016	3,519.59 -	05/2019 -	-
49	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL, MULTI STATE	03/2017	283.72 -	11/2019 -	-
50	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL, MULTI STATE	10/2016	608.24 -	04/2019 -	-
51	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL, MULTI STATE	12/2015	3,654.00 -	04/2019 -	-

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	Total		95,740.17		
	<u>HEAVY INDUSTRY</u>				
	<u>Bharat Heavy Electricals Limited</u>				
52	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL,DELHI	08/2016	1,554.00	09/2019	-
	Total		1,554.00		
	<u>HEALTH AND FAMILY WELFARE</u>				
	<u>Hospital Services Consultancy Corporation Ltd</u>				
53	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57	12/2014	03/2018
54	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL	08/2016	244.00	09/2018	05/2019
55	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL	12/2014	168.90	05/2017	07/2019
56	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA	09/2014	505.58	03/2018	09/2019
57	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65	05/2017	01/2020
58	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19	03/2019	01/2021
59	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA	01/2018	249.01	-	01/2021
60	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44	05/2017	03/2021
61	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95	02/2018	03/2021
62	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19	03/2019	03/2021
63	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH	03/2018	268.84	-	03/2021
	Total		2,809.32		
	<u>RAILWAYS</u>				
	<u>Central Railways</u>				
64	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06	03/2019	-
	<u>Container Corporation Of India</u>				
65	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH	01/2013	387.70	03/2018	03/2021
66	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00	03/2019	12/2020
67	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32	03/2019	03/2021

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
68	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI, RAJASTHAN	01/2011	493.17 -	03/2018 -	-
69	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI, CHHATISGARH	05/2014	207.00 -	03/2018 -	-
70	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI, MADHYA PRADESH	12/2015	174.00 -	03/2019 -	-
71	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI, GUJARAT	10/2013	343.00 -	03/2019 -	-
72	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI, ANDHRA PRADESH	08/2016	234.50 -	03/2019 -	-
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>				
73	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC, MULTI STATE	10/2006	11,589.00 30,357.00	- -	-
74	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC, MULTI STATE	11/2007	16,592.00 51,101.00	03/2020 -	-
	<u>East Central Railways</u>				
75	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR, BIHAR	04/1999	325.00 -	- -	03/2021
76	KOSI BRIDGE (NL), ECR - [220100304]ECR, BIHAR	04/2002	499.41 -	03/2020 -	-
77	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR, BIHAR	04/2001	406.92 -	- -	-
78	ARA-BHABHUA ROAD (NL) - [N22000166]ECR, BIHAR	04/2008	633.87 -	- -	-
79	NAWADA-LAXMIPUR (NL) - [N22000167]ECR, BIHAR	04/2008	620.57 -	- -	-
80	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR, BIHAR	04/2008	445.25 -	- -	-
81	GAYA-CHATRA (NL) - [N22000169]ECR, MULTI STATE	04/2008	415.67 -	- -	-
82	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR, BIHAR	04/2005	205.00 -	- -	-
83	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR, BIHAR	04/2006	211.00 -	- -	-
84	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR, BIHAR	04/2008	678.62 -	- -	-
85	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR, BIHAR	04/2008	192.56 -	- -	-
86	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR, BIHAR	04/2008	281.30 -	- -	-
87	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR, BIHAR	04/2013	213.01 -	- -	-
88	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR, BIHAR	01/1991	332.15 -	07/2014 -	-
89	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR, BIHAR	04/1998	180.82 -	- -	-
	<u>Eastern Railways</u>				
90	PIRPAINTI-BHAGALPUR - [N22000222]ER, MULTI STATE	04/2011	261.38 -	- -	05/2019

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
91	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	03/2021
92	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	11/2018 -	03/2021
93	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	542.18 -	03/2020 -	03/2021
	<u>Kolkata Metro Rail Corporation Limited</u>				
94	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-
	<u>Metropolitan Rapid Transport Projects</u>				
95	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT (MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-
96	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 -	03/2014 -	-
97	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	-
	<u>North Central Railway</u>				
98	ETAWAH-MAINPURI (NL), NCR - [220100318]NCR, UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-
99	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR, MULTI STATE	04/2010	2,030.50 -	- -	-
100	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR, UTTAR PRADESH	04/2015	668.70 668.00	03/2020 -	-
101	JHANSI BINA DOUBLING - [N22000496]NCR, UTTAR PRADESH	09/2016	2,001.00 -	03/2021 -	-
	<u>North East Frontier Railway</u>				
102	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR, ASSAM	04/2011	314.00 486.96	03/2019 -	03/2021
103	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR (NL), NEFR - [220100135]NFR, WEST BENGAL	04/1983	297.32 200.34	03/2019 -	-
104	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48 -	12/2015 -	-
105	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 -	- -	-
106	DIMAPUR-TIZIT NL - [N22000196]NFR, NAGALAND	04/2013	4,274.00 -	03/2020 -	-
107	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR, MEGHALAYA	04/2010	906.46 1,202.33	03/2021 -	-
108	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR, MULTI STATE	04/2010	242.22 -	03/2020 -	-
109	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR, MULTI STATE	04/1999	819.23 -	- -	-
110	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHOWA-JAIN - [N22000499]NFR, WEST BENGAL	02/1999	380.60 -	04/2010 -	-
111	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR, BIHAR	04/2008	333.76 -	- -	-

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
112	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	414.84 -	03/2020 -	-
	<u>North Eastern Railway</u>				
113	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH	04/2017	622.50 427.00	04/2017 -	03/2021
114	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-
115	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
116	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
117	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-
118	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-
	<u>North Western Railway</u>				
119	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	10/2018 -	01/2020
120	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	02/2019 -	02/2020
121	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	12/2019 -	02/2021
122	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	11/2019 -	03/2021
123	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-
124	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
125	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
126	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-
	<u>Northern Railway</u>				
127	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
	<u>Rail India Technical And Economic Service</u>				
128	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES,TELANGANA	03/2015	636.38 -	03/2021 -	03/2021
129	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-
	<u>Rail Vikas Nigam Ltd.</u>				
130	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT	04/2012	644.38 -	03/2021 -	03/2021
131	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	1,185.64 -	12/2017 -	-
132	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	03/2009 03/2009	-
	<u>Railway Electrification</u>				

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
133	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-
	<u>South Central Railway</u>				
134	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	164.36 -	02/2009 -	-
135	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-
136	GUDUR-DURGARA JAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	761.37 -	- -	-
137	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
138	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-
	<u>South East Central Railway</u>				
139	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- -	-
140	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR,CHHATISGARH	04/2008	872.00 -	12/2019 -	-
	<u>South Eastern Railway</u>				
141	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	12/2016 -	08/2020
142	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-
143	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-
	<u>Southern Railway</u>				
144	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU	10/2013	187.26 -	04/2014 -	12/2020
145	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	1,566.00 -	- -	-
146	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	227.40 -	- -	-
147	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	151.84 -	02/2019 -	-
148	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
149	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
150	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
151	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-
152	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 -	- -	-
153	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	- -	-
154	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
155	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU	02/1999	257.00 257.00	03/2018 -	-
	<u>Western Railway</u>				
156	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT	04/2017	691.84 1,017.91	03/2020 02/2021	02/2021
157	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-
158	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT	03/2017	243.60 -	- -	-
159	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-
160	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-
161	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-
162	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 -	- -	-
	Total		91,046.77 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
	<u>Central Public Works Department</u>				
163	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE - [N24001236]CPWD,TAMIL NADU	03/2019	297.55 -	11/2019 -	-
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>				
164	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]MoRTH,ANDHRA PRADESH	03/2018	504.19 504.00	11/2018 -	01/2021
165	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]MoRTH,ANDHRA PRADESH	03/2018	289.67 290.00	08/2018 -	02/2021
166	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]MoRTH,ANDHRA PRADESH	03/2015	271.45 -	10/2015 -	03/2021
167	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH	01/2012	410.72 -	04/2015 -	03/2021
168	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934]MoRTH,ANDHRA PRADESH	03/2018	228.32 -	08/2018 -	03/2021
169	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950]MoRTH,RAJASTHAN	11/2017	187.82 -	04/2018 -	03/2021
170	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709 - [N24000957]MoRTH,RAJASTHAN	11/2017	163.95 -	04/2018 -	03/2021
171	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MoRTH,RAJASTHAN	03/2019	178.13 -	- -	03/2021

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
172	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932]MoRTH,ANDHRA PRADESH	01/2017	319.28 -	08/2017 -	08/2019
173	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. - [N24001174]MoRTH,MANIPUR	10/2016	235.31 -	11/2020 -	11/2020
174	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]MoRTH,NAGALAND	03/2017	217.35 -	11/2020 05/2021	11/2020
175	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]MoRTH,MIZORAM	11/2010	624.41 -	03/2011 -	12/2020
176	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]MoRTH,PUNJAB	11/2015	889.24 -	- -	12/2020
177	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964]MoRTH,ANDHRA PRADESH	08/2016	350.61 -	01/2017 -	12/2020
178	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]MoRTH,NAGALAND	10/2016	167.62 -	12/2020 09/2021	12/2020
179	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]MoRTH,NAGALAND	10/2016	172.63 -	12/2020 09/2021	12/2020
180	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]MoRTH,WEST BENGAL	04/2014	279.70 398.52	08/2017 01/2020	02/2020
181	R AND U FROM KM 385.00 TO KM 420.000 TO 2- LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404 - [N24001205]MoRTH,UTTAR PRADESH	12/2016	209.10 -	10/2019 -	04/2020
182	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]MoRTH,CHHATISGARH	11/2015	485.44 -	12/2015 05/2020	05/2020
183	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH,ARUNACHAL PRADESH	11/2016	243.89 -	- -	09/2020
184	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 127.500 TO 178.944 DARRIGHAT TO BANARI SECTION - [N24001220]MoRTH,CHHATISGARH	03/2016	491.52 512.77	09/2016 10/2020	10/2020
185	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884]MoRTH,MADHYA PRADESH	03/2018	191.21 -	11/2019 -	01/2021
186	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L - [N24001131]MoRTH,JHARKHAND	03/2018	212.99 -	06/2020 -	01/2021
187	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH - [N24001145]MoRTH,UTTAR PRADESH	05/2013	164.54 165.00	08/2015 -	01/2021
188	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]MoRTH,UTTAR PRADESH	03/2018	185.18 -	02/2020 -	01/2021
189	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]MoRTH,MADHYA PRADESH	11/2017	235.91 -	02/2018 02/2021	02/2021

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
190	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]MoRTH,HARYANA	01/2017	247.25 -	03/2019 -	02/2021
191	REHABILITATION AND UPGRADATION OF HARPALPUR -SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE - [N24000942]MoRTH,UTTAR PRADESH	03/2016	208.50 -	11/2019 -	02/2021
192	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883]MoRTH,WEST BENGAL	03/2018	254.30 254.30	10/2020 -	03/2021
193	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH,UTTAR PRADESH	03/2016	240.30 240.00	01/2020 -	03/2021
194	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]MoRTH,UTTAR PRADESH	03/2016	249.50 -	05/2019 -	03/2021
195	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203]MoRTH,UTTAR PRADESH	10/2016	218.90 -	03/2020 -	03/2021
196	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]MoRTH,UTTAR PRADESH	07/2016	208.88 -	10/2019 -	03/2021
197	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208]MoRTH,UTTAR PRADESH	03/2018	288.30 -	08/2020 -	03/2021
198	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO - [N24001224]MoRTH,CHHATISGARH	03/2017	423.79 -	01/2018 03/2021	03/2021
199	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]MoRTH,TELANGANA	01/2014	270.00 -	03/2016 -	-
200	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA	03/2015	153.21 -	01/2017 -	-
201	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]MoRTH,GOA	03/2015	297.00 -	04/2018 -	-
202	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]MoRTH,MAHARASHTRA	03/2015	168.30 -	- -	-
203	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]MoRTH,MAHARASHTRA	08/2014	187.79 -	07/2016 -	-
204	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]MoRTH,MAHARASHTRA	01/2014	446.77 -	- -	-
205	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]MoRTH,GOA	03/2015	298.33 -	- -	-
206	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]MoRTH,GOA	03/2015	184.05 -	- -	-
207	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]MoRTH,GOA	03/2015	280.16 -	- -	-
208	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]MoRTH,KERALA	01/2014	255.75 348.00	09/2017 -	-

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
209	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]MoRTH,ANDHRA PRADESH	07/2015	333.21 333.21	12/2015 -	-
210	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MoRTH,MAHARASHTRA	10/2015	289.60 -	- -	-
211	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MoRTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-
212	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]MoRTH,ANDHRA PRADESH	01/2014	195.45 -	11/2014 -	-
213	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MoRTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-
214	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MoRTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-
215	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MoRTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-
216	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MoRTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-
217	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MoRTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-
218	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]MoRTH,ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	-
219	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]MoRTH,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-
220	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]MoRTH,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-
221	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]MoRTH,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 06/2018	-
222	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]MoRTH,NAGALAND	12/2010	1,296.00 -	02/2011 -	-
223	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MoRTH,TAMIL NADU	03/2015	258.97 -	08/2015 -	-
224	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MoRTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-
225	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - - [N24000318]MoRTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-
226	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MoRTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-
227	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA	01/2015	225.81 -	- -	-

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
228	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MoRTH,RAJASTHAN	12/2015	621.43 -	06/2018 -	-
229	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-
230	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MoRTH,KARNATAKA	03/2015	159.12 -	11/2015 -	-
231	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]MoRTH,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	-
232	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]MoRTH,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	-
233	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]MoRTH,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	-
234	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MoRTH,KARNATAKA	01/1991	219.40 -	01/2018 -	-
235	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MoRTH,ODISHA	01/1991	218.63 -	10/2017 -	-
236	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH,BIHAR	01/1991	675.00 -	- -	-
237	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]MoRTH,PUNJAB	12/2015	766.36 -	- -	-
238	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]MoRTH,PUNJAB	11/2015	847.02 -	- -	-
239	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]MoRTH,ASSAM	11/2010	268.08 -	05/2017 -	-
240	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]MoRTH,MADHYA PRADESH	08/2015	257.80 -	- -	-
241	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]MoRTH,ASSAM	11/2010	470.20 -	02/2011 -	-
242	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MoRTH,WEST BENGAL	01/1991	322.00 -	03/2018 -	-
243	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MoRTH,BIHAR	01/1991	282.41 -	08/2016 -	-
244	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MoRTH,BIHAR	01/1991	358.22 -	10/2016 -	-
245	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]MoRTH,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-
246	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MoRTH,ODISHA	01/1991	229.41 -	05/2018 -	-

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
247	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]MoRTH,ODISHA	07/2014	342.05 -	01/2017 -	-
248	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH,GOA	10/2015	936.40 -	- -	-
249	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]MoRTH,RAJASTHAN	09/2012	511.00 -	10/2013 -	-
250	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]MoRTH,RAJASTHAN	09/2012	511.00 -	10/2013 -	-
251	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	-
252	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH,GOA	12/2015	773.98 -	- -	-
253	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MoRTH,GOA	12/2015	819.95 -	- -	-
254	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MoRTH,BIHAR	01/1991	478.35 -	- -	-
255	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]MoRTH,ODISHA	12/2011	159.39 -	11/2017 -	-
256	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]MoRTH,PUNJAB	06/2015	892.17 -	- -	-
257	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH,ODISHA	12/2011	191.08 -	08/2015 -	-
258	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]MoRTH,BIHAR	01/1991	154.62 -	- -	-
259	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]MoRTH,BIHAR	01/1991	319.68 -	- -	-
260	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MoRTH,BIHAR	10/2013	278.39 -	08/2014 -	-
261	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MoRTH,BIHAR	11/2013	683.83 -	07/2016 -	-
262	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MoRTH,BIHAR	02/2014	665.50 -	07/2016 -	-
263	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MoRTH,BIHAR	02/2016	178.85 -	05/2016 -	-
264	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MoRTH,BIHAR	02/2016	369.77 -	06/2016 -	-
265	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MoRTH,BIHAR	02/2016	553.30 -	05/2016 -	-

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
266	FOUR LANNING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-
267	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPR - [N24000580]MoRTH,BIHAR	03/2015	206.80 -	07/2016 -	-
268	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MoRTH,BIHAR	08/2015	288.24 -	11/2015 -	-
269	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH,MAHARASHTRA	03/2016	1,142.62 -	- -	-
270	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH,MAHARASHTRA	03/2016	1,101.58 -	- -	-
271	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH,BIHAR	08/2016	1,742.01 -	12/2016 -	-
272	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH,ODISHA	03/2014	191.50 192.00	05/2016 -	-
273	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MoRTH,ODISHA	01/2015	326.63 327.00	04/2018 -	-
274	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MoRTH,ODISHA	02/2015	239.91 240.00	10/2017 -	-
275	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MoRTH,ODISHA	07/2014	342.05 342.00	01/2017 -	-
276	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH,ODISHA	08/2013	171.96 172.00	06/2016 -	-
277	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MoRTH,ODISHA	06/2016	157.30 157.00	06/2018 -	-
278	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH,UTTARAKHAND	12/2017	257.34 -	12/2019 -	-
279	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH,UTTARAKHAND	12/2017	200.34 -	12/2019 -	-
280	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MoRTH,UTTARAKHAND	12/2017	248.22 -	12/2019 -	-
281	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MoRTH,UTTARAKHAND	06/2017	282.08 -	06/2019 -	-
282	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH,UTTARAKHAND	11/2017	232.81 -	11/2019 -	-
283	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH,UTTARAKHAND	11/2017	283.51 -	11/2019 -	-
284	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH,UTTARAKHAND	11/2017	266.52 -	11/2019 -	-

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
285	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MoRTH,UTTARAKHAND	02/2018	418.88 -	02/2020 -	-
286	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MoRTH,UTTARAKHAND	02/2018	293.68 -	- -	-
287	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MoRTH,UTTARAKHAND	05/2018	248.00 -	05/2020 -	-
288	REHABILITATION AND UPGADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH,UTTARAKHAND	03/2018	460.73 -	- -	-
289	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MoRTH,A & N ISLANDS	11/2017	237.80 -	11/2019 -	-
290	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH,A & N ISLANDS	11/2017	257.34 -	11/2019 -	-
291	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O - [N24000871]MoRTH,WEST BENGAL	08/2014	600.87 720.97	11/2017 -	-
292	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH	03/2018	166.21 -	08/2018 -	-
293	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873]MoRTH,WEST BENGAL	08/2014	823.20 937.76	11/2017 -	-
294	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879]MoRTH,WEST BENGAL	03/2017	202.69 202.69	11/2019 -	-
295	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906]MoRTH,PUNJAB	03/2018	173.24 -	06/2020 -	-
296	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]MoRTH,PUNJAB	03/2018	293.10 -	08/2020 -	-
297	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) - [N24000908]MoRTH,HARYANA	01/2017	276.01 -	03/2019 -	-
298	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26. - [N24000911]MoRTH,ODISHA	03/2016	165.06 -	12/2016 -	-
299	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MoRTH,ODISHA	08/2016	287.70 -	02/2017 -	-
300	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH,ODISHA	09/2016	295.67 -	02/2017 -	-
301	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH,ODISHA	12/2016	223.50 -	08/2018 -	-
302	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH,ODISHA	12/2016	206.88 -	04/2018 -	-
303	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH,ODISHA	03/2018	214.23 -	08/2018 -	-
304	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH,ODISHA	03/2018	199.16 -	08/2018 -	-

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
305	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922]MoRTH,GUJARAT	12/2017	867.97 -	11/2018 -	-
306	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEEN - [N24000923]MoRTH,GUJARAT	03/2018	464.07 -	11/2018 -	-
307	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]MoRTH,GUJARAT	10/2018	400.76 -	05/2019 -	-
308	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926]MoRTH,GUJARAT	08/2017	962.43 -	03/2018 -	-
309	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000927]MoRTH,PUNJAB	03/2018	293.64 -	08/2020 -	-
310	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH 0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]MoRTH,ANDHRA PRADESH	10/2015	333.21 -	12/2015 -	-
311	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO - [N24000930]MoRTH,ANDHRA PRADESH	11/2016	378.24 -	01/2018 -	-
312	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU - [N24000936]MoRTH,ANDHRA PRADESH	03/2018	244.95 245.00	08/2018 -	-
313	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938]MoRTH,ANDHRA PRADESH	03/2018	297.12 294.00	07/2018 -	-
314	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]MoRTH,PUNJAB	03/2018	293.64 -	08/2020 -	-
315	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR	09/2018	1,478.40 -	- -	-
316	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 - [N24000962]MoRTH,MADHYA PRADESH	09/2016	178.23 -	09/2018 -	-
317	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]MoRTH,ANDHRA PRADESH	01/2016	386.09 -	05/2016 -	-
318	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967]MoRTH,ANDHRA PRADESH	03/2016	444.84 -	09/2016 -	-
319	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]MoRTH,ANDHRA PRADESH	11/2016	376.25 -	08/2017 -	-
320	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]MoRTH,ANDHRA PRADESH	01/2017	576.48 -	01/2018 -	-
321	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA	10/2016	298.32 -	02/2019 -	-
322	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA	10/2016	248.83 -	03/2019 -	-

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
323	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037 OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH, TELANGANA	01/2017	244.54 -	05/2019 -	-
324	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]MoRTH, TELANGANA	01/2017	196.52 -	10/2019 -	-
325	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]MoRTH, TELANGANA	01/2017	283.00 -	12/2019 -	-
326	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]MoRTH, TELANGANA	01/2017	359.27 -	05/2019 -	-
327	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH, TELANGANA	01/2017	300.00 -	05/2019 -	-
328	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]MoRTH, TELANGANA	01/2018	283.15 -	05/2020 -	-
329	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]MoRTH, TELANGANA	01/2018	230.03 -	12/2019 -	-
330	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]MoRTH, TELANGANA	02/2018	206.13 -	06/2020 -	-
331	REHABILITATION AND UPGADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH, TELANGANA	02/2018	294.13 -	11/2019 -	-
332	REHABILITATION AND UPGADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH, TELANGANA	02/2018	220.28 -	11/2019 -	-
333	REHABILITATION AND UPGADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]MoRTH, TELANGANA	02/2018	426.52 -	04/2020 -	-
334	REHABILITATION AND UPGADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]MoRTH, TELANGANA	03/2018	322.81 -	09/2020 -	-
335	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]MoRTH, TELANGANA	03/2018	626.76 -	07/2020 -	-
336	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH, TELANGANA	01/2017	605.08 -	10/2019 -	-
337	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL - MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH, TELANGANA	03/2018	192.67 -	07/2019 -	-
338	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH, TELANGANA	01/2019	193.19 -	- -	-
339	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C - [N24000999]MoRTH, BIHAR	11/2016	230.34 -	10/2019 -	-
340	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH, BIHAR	03/2018	153.24 -	- -	-

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
341	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC - [N24001001]MoRTH,BIHAR	05/2014	199.98 -	08/2016 -	-
342	SARSAM TO KOTHARI - [N24001002]MoRTH,MAHARASHTRA	02/2016	545.64 -	07/2019 -	-
343	AKOLA TO AKOT - [N24001003]MoRTH,MAHARASHTRA	01/2017	313.95 -	06/2019 -	-
344	PATRADEVI TO KARASWADA 4L - [N24001004]MoRTH,GOA	03/2017	634.32 -	05/2020 -	-
345	KARASWADA TO BAMBOLIM - [N24001005]MoRTH,GOA	03/2017	852.67 -	12/2019 -	-
346	AKOT TO ANJANGAON - [N24001006]MoRTH,MAHARASHTRA	01/2017	245.77 246.00	06/2019 -	-
347	ANJANGAON TO MAH/MP BORDER - [N24001007]MoRTH,MADHYA PRADESH	01/2017	359.00 359.00	06/2019 -	-
348	AJANTHA TO BULDHANA - [N24001008]MoRTH,A & N ISLANDS	02/2017	401.00 401.00	07/2019 -	-
349	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA	02/2017	203.21 203.00	05/2019 -	-
350	SHEGAON TO DEORI PHATA - [N24001010]MoRTH,MAHARASHTRA	02/2017	373.10 373.00	05/2019 -	-
351	MEHKAR TO CHIKALI - [N24001011]MoRTH,MAHARASHTRA	02/2017	322.48 322.00	05/2019 -	-
352	CHIKALI TO KHAMGAON - [N24001012]MoRTH,MAHARASHTRA	02/2017	548.03 548.00	06/2019 -	-
353	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA	01/2017	391.06 391.00	06/2019 -	-
354	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA	01/2017	385.87 386.00	06/2019 -	-
355	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA	01/2017	341.16 341.00	06/2019 -	-
356	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH,MAHARASHTRA	01/2017	471.61 472.00	06/2019 -	-
357	DAHEGAON TO KUHI - [N24001017]MoRTH,MAHARASHTRA	01/2017	228.89 229.00	06/2019 -	-
358	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA	01/2017	392.83 393.00	06/2019 -	-
359	KATOL TO WARUD - [N24001019]MoRTH,MAHARASHTRA	01/2017	463.62 664.00	06/2019 -	-
360	AMDHI TO SAONER - [N24001021]MoRTH,MAHARASHTRA	01/2017	396.91 397.00	06/2019 -	-
361	WADI TO ASOLA - [N24001022]MoRTH,MAHARASHTRA	01/2017	363.82 364.00	09/2019 -	-
362	NAGAJ TO VAJJAPUR - [N24001023]MoRTH,MAHARASHTRA	01/2017	376.72 377.00	06/2019 -	-
363	MANGAON TO DIGHI PORT - [N24001024]MoRTH,MAHARASHTRA	01/2017	457.52 -	07/2019 -	-
364	INDAPUR TO AGARDANDA - [N24001025]MoRTH,MAHARASHTRA	01/2017	355.17 -	07/2019 -	-
365	WAKAN PALI KHOPOLI - [N24001026]MoRTH,MAHARASHTRA	01/2017	376.19 -	05/2019 -	-

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
366	SHAHPUR PATGAON SECTION I - [N24001027]MoRTH,MAHARASHTRA	01/2018	150.79 -	12/2019 -	-
367	PATGAON KHOPOLI SECTION I - [N24001028]MoRTH,MAHARASHTRA	01/2018	170.00 -	12/2019 -	-
368	AHMADPUR TO PIMPLA - [N24001029]MoRTH,MAHARASHTRA	01/2017	422.38 -	08/2019 -	-
369	PIMPLA TO MANJARSUMBHA - [N24001030]MoRTH,MAHARASHTRA	01/2017	595.77 -	08/2019 -	-
370	MANJUSUMBA TO CHUMBALI - [N24001031]MoRTH,MAHARASHTRA	01/2017	228.54 -	08/2019 -	-
371	DEORI TO AMGAON - [N24001032]MoRTH,MAHARASHTRA	01/2017	409.62 410.00	05/2019 -	-
372	MANTHA TALUKAS BORDER TO PARTUR - [N24001033]MoRTH,MAHARASHTRA	01/2017	486.19 -	07/2019 -	-
373	PARTUR TO MAJALGAON - [N24001034]MoRTH,MAHARASHTRA	01/2017	420.57 -	07/2019 -	-
374	MANSAR TO SALAIKHURD - [N24001035]MoRTH,MAHARASHTRA	01/2018	418.36 -	12/2019 -	-
375	MAJALGAON TO KAIJ - [N24001036]MoRTH,MAHARASHTRA	01/2017	413.99 -	07/2019 -	-
376	KAIJ TO KUSALAM - [N24001037]MoRTH,MAHARASHTRA	01/2017	554.78 -	07/2019 -	-
377	MAHAD TO RAIGAD FORT - [N24001038]MoRTH,MAHARASHTRA	07/2018	237.40 -	05/2020 -	-
378	JINTUR TO PARBHANI - [N24001039]MoRTH,MAHARASHTRA	01/2017	356.66 -	- -	-
379	JAHIRABAD TO LATUR - [N24001040]MoRTH,MAHARASHTRA	01/2017	461.96 -	11/2019 -	-
380	SHIROD SHAHPURER TO NANDED - [N24001041]MoRTH,MAHARASHTRA	01/2017	211.34 -	07/2019 -	-
381	SALAIKHURD TO TIRORA - [N24001042]MoRTH,MAHARASHTRA	01/2018	415.25 415.25	12/2019 -	-
382	NILAJPHATA TO BHANDARA - [N24001043]MoRTH,MAHARASHTRA	01/2018	420.63 421.00	05/2020 -	-
383	KALMAB TO RALEGAON - [N24001044]MoRTH,MAHARASHTRA	01/2017	467.78 -	06/2019 -	-
384	JALGAON TO BHADGAON - [N24001045]MoRTH,MAHARASHTRA	01/2018	307.54 308.00	11/2019 -	-
385	RALEGAON TO RAMTIRTH - [N24001046]MoRTH,MAHARASHTRA	01/2017	210.81 -	07/2019 -	-
386	BHADGAON TO CHALISGAON - [N24001047]MoRTH,MAHARASHTRA	01/2018	259.55 260.00	11/2019 -	-
387	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA	01/2017	232.77 -	07/2019 -	-
388	KARAD TO VITA - [N24001049]MoRTH,MAHARASHTRA	01/2018	344.85 245.00	12/2019 -	-
389	VITA TO NAGAJ - [N24001050]MoRTH,MAHARASHTRA	03/2018	304.58 305.00	12/2019 -	-
390	NALDURG TO AKKALKOT - [N24001051]MoRTH,MAHARASHTRA	02/2018	274.50 275.00	12/2019 -	-

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
391	SANGOLA TO JATH - [N24001052]MoRTH,MAHARASHTRA	01/2018	257.38 257.00	12/2019 -	-
392	KARAD TO TAGAON - [N24001053]MoRTH,MAHARASHTRA	01/2017	537.81 538.00	06/2019 -	-
393	TASGAON TO SHIRDHON - [N24001054]MoRTH,MAHARASHTRA	01/2017	195.64 196.00	11/2019 -	-
394	HELWAK TO KARAD - [N24001055]MoRTH,MAHARASHTRA	02/2017	416.99 -	07/2019 -	-
395	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA	02/2017	422.02 422.00	07/2019 -	-
396	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MoRTH,MAHARASHTRA	02/2017	407.19 407.00	06/2019 -	-
397	KARWANDI TO RAJURI - [N24001058]MoRTH,MAHARASHTRA	03/2018	276.95 277.00	12/2019 -	-
398	SHIVUR TO YEOLA - [N24001059]MoRTH,MAHARASHTRA	03/2018	181.08 -	12/2019 -	-
399	PALPHATA TO PHULAMBARI - [N24001060]MoRTH,MAHARASHTRA	03/2018	227.19 227.00	12/2019 -	-
400	CHIKALI TO DHAD - [N24001061]MoRTH,MAHARASHTRA	03/2018	189.46 189.00	12/2019 -	-
401	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]MoRTH,MAHARASHTRA	03/2018	336.21 336.00	12/2019 -	-
402	WADIGODRI TO DHANGRIPIMPRI - [N24001063]MoRTH,MAHARASHTRA	03/2018	194.23 194.00	02/2020 -	-
403	DHANGRIPIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]MoRTH,MAHARASHTRA	03/2018	217.14 217.00	02/2020 -	-
404	PARBHANI TO GANGKHED - [N24001065]MoRTH,MAHARASHTRA	03/2018	238.19 238.00	12/2019 -	-
405	LATUR TO PANGAON - [N24001066]MoRTH,MAHARASHTRA	03/2018	336.47 336.00	12/2019 -	-
406	OMREGA TO AUSA - [N24001067]MoRTH,MAHARASHTRA	03/2018	272.04 272.00	12/2019 -	-
407	WASHIM TO DASTAPUR - [N24001068]MoRTH,MAHARASHTRA	03/2018	165.51 -	12/2019 -	-
408	NANDED TO JALKOT - [N24001069]MoRTH,MAHARASHTRA	12/2017	456.93 457.00	09/2019 -	-
409	DASTAPUR TO KARANJA - [N24001070]MoRTH,MAHARASHTRA	03/2018	182.63 -	12/2019 -	-
410	JALKOT TO TOGRI - [N24001071]MoRTH,MAHARASHTRA	07/2018	299.92 300.00	08/2020 -	-
411	KHERDA TO NAGZARI - [N24001072]MoRTH,MAHARASHTRA	03/2018	181.30 -	12/2019 -	-
412	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA	09/2018	301.38 301.00	08/2020 -	-
413	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA	03/2018	249.29 -	12/2019 -	-
414	OSMANNAGAR TO KUNDRAL - [N24001075]MoRTH,MAHARASHTRA	09/2017	344.25 344.00	08/2020 -	-
415	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA	03/2018	219.91 -	12/2019 -	-

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
416	KUNDRAL TO WAZAR - [N24001077]MoRTH,MAHARASHTRA	01/2018	225.25 225.00	12/2019 -	-
417	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA	03/2018	228.31 -	12/2019 -	-
418	ARDHAPUR TO HIMAYATNAGAR - [N24001079]MoRTH,MAHARASHTRA	12/2017	426.06 426.00	06/2020 -	-
419	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA	03/2018	256.15 -	12/2019 -	-
420	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]MoRTH,MAHARASHTRA	03/2018	294.87 295.00	12/2019 -	-
421	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA	03/2018	223.46 -	12/2019 -	-
422	CHIKLI TO TAKARKHED - [N24001083]MoRTH,MAHARASHTRA	03/2018	393.10 393.00	12/2019 -	-
423	PAHUR TO BODHWAD - [N24001084]MoRTH,MAHARASHTRA	01/2017	244.93 -	05/2020 -	-
424	TAKARKHED TO JALNA - [N24001085]MoRTH,MAHARASHTRA	09/2017	417.90 418.00	06/2019 -	-
425	BODHWAD TO STATE BORDER - [N24001086]MoRTH,MAHARASHTRA	01/2017	178.26 -	07/2019 -	-
426	MANGRUPHIR TO MAHAN - [N24001087]MoRTH,MAHARASHTRA	03/2018	222.13 222.00	11/2019 -	-
427	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA	03/2018	177.84 177.00	12/2019 -	-
428	MALEGAON TO RISOD - [N24001089]MoRTH,MAHARASHTRA	02/2018	303.24 303.00	12/2019 -	-
429	KOLDE TO KHETIYA - [N24001090]MoRTH,MAHARASHTRA	01/2017	509.18 -	07/2019 -	-
430	SATARA TO MHASWAD - [N24001092]MoRTH,MAHARASHTRA	01/2017	653.46 -	07/2019 -	-
431	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA	12/2017	309.94 310.00	12/2019 -	-
432	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA	12/2017	244.04 244.00	03/2019 -	-
433	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA	01/2017	388.44 -	- -	-
434	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA	01/2018	264.41 264.00	03/2019 -	-
435	SELDOH TO PANVAR - [N24001097]MoRTH,MAHARASHTRA	07/2018	404.33 404.00	05/2020 -	-
436	WARDHA TO HINGAGHAT - [N24001098]MoRTH,MAHARASHTRA	01/2018	216.90 217.00	12/2019 -	-
437	MHASWAD TO TEMBHURNI - [N24001099]MoRTH,MAHARASHTRA	01/2017	488.60 -	07/2019 -	-
438	AHMEDNAGAR TO BARAMATI - [N24001100]MoRTH,MAHARASHTRA	01/2017	955.40 -	08/2019 -	-
439	KURUDWADI TO PANDHARPUR - [N24001101]MoRTH,MAHARASHTRA	01/2017	307.63 -	07/2019 -	-
440	PANDHARPUR TO SANGOLA - [N24001102]MoRTH,MAHARASHTRA	07/2017	218.38 -	07/2019 -	-

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
441	SARAD VANI PIMPALGAON - [N24001103]MoRTH,MAHARASHTRA	01/2017	250.46 -	07/2019 -	-
442	MALEWADA TO CHIMUR - [N24001104]MoRTH,MAHARASHTRA	10/2016	322.55 -	06/2019 -	-
443	CHIMUR TO WARORA - [N24001105]MoRTH,MAHARASHTRA	11/2016	467.70 -	03/2019 -	-
444	PEN TO KHOPOLI - [N24001106]MoRTH,MAHARASHTRA	03/2018	301.39 302.00	03/2018 -	-
445	PANCHARAL TO MANDANGHAR - [N24001107]MoRTH,MAHARASHTRA	07/2018	381.08 302.00	05/2020 -	-
446	CHALISGAON TO NANDGAON - [N24001108]MoRTH,MAHARASHTRA	03/2018	206.97 207.00	12/2019 -	-
447	KUSUMBA TO MALEGAON - [N24001109]MoRTH,MAHARASHTRA	03/2018	243.45 244.00	12/2019 -	-
448	BAMNI TO NAVAEGAON - [N24001110]MoRTH,MAHARASHTRA	09/2017	241.69 242.00	04/2020 -	-
449	KOLHA TO NASRATPUR - [N24001111]MoRTH,MAHARASHTRA	04/2016	281.78 282.00	04/2019 -	-
450	NASRATPUR TO BARASGAON - [N24001112]MoRTH,MAHARASHTRA	07/2016	406.54 407.00	09/2019 -	-
451	INDAPUR TO VADPALE - [N24001114]MoRTH,MAHARASHTRA	01/2017	1,202.52 1,203.00	12/2019 -	-
452	VADPALE TO BHOGAN KHURD - [N24001115]MoRTH,MAHARASHTRA	01/2017	1,598.47 1,560.00	11/2019 -	-
453	GADCHIROLI TO MUL - [N24001116]MoRTH,MAHARASHTRA	12/2016	484.15 -	06/2019 -	-
454	MUL TO CHANDRAPUR - [N24001117]MoRTH,MAHARASHTRA	12/2016	162.34 -	07/2019 -	-
455	SAKOLI TO BHANDARA - [N24001118]MoRTH,MAHARASHTRA	01/2017	362.96 -	06/2019 -	-
456	NAGBHID TO ARMORI - [N24001119]MoRTH,MAHARASHTRA	09/2016	269.05 -	07/2019 -	-
457	AKKALKOT TO DHUDHNI - [N24001120]MoRTH,MAHARASHTRA	04/2016	211.42 -	02/2019 -	-
458	NASHIK TO PETH - [N24001121]MoRTH,MAHARASHTRA	12/2015	289.60 -	11/2018 -	-
459	PAITHAN TO SHIRUR - [N24001122]MoRTH,MAHARASHTRA	03/2017	341.80 -	06/2019 -	-
460	SHIRUR TO KHARDA - [N24001123]MoRTH,MAHARASHTRA	02/2017	381.77 -	06/2019 -	-
461	AURANGABAD TO SILLOD - [N24001124]MoRTH,MAHARASHTRA	02/2017	456.32 -	06/2019 -	-
462	SILLOD TO FARDAPUR - [N24001125]MoRTH,MAHARASHTRA	02/2017	337.46 -	06/2019 -	-
463	FARDAPUR TO JALGAON - [N24001126]MoRTH,MAHARASHTRA	02/2017	456.45 -	06/2019 -	-
464	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA	02/2017	406.51 -	06/2019 -	-
465	BHOKAR TO SARSAM - [N24001128]MoRTH,MAHARASHTRA	02/2017	295.09 -	07/2019 -	-

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
466	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND	08/2016	234.88 -	12/2017 -	-
467	PARSHURAM GHAT TO ARAWALI - [N24001133]MoRTH,MAHARASHTRA	04/2016	983.14 983.00	12/2019 -	-
468	KANTE TO WAKED - [N24001134]MoRTH,MAHARASHTRA	03/2016	1,230.02 1,230.00	11/2019 -	-
469	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	-
470	TALGAON TO KALMATH - [N24001136]MoRTH,MAHARASHTRA	10/2016	904.70 905.00	03/2020 -	-
471	KALMATH TO ZARAP - [N24001137]MoRTH,MAHARASHTRA	09/2016	1,338.13 1,338.00	03/2020 -	-
472	PARLI PIMPLA DAHIGUDA - [N24001138]MoRTH,MAHARASHTRA	02/2017	205.72 206.00	06/2019 -	-
473	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA - [N24001139]MoRTH,UTTAR PRADESH	10/2016	218.94 219.00	03/2020 -	-
474	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]MoRTH,UTTAR PRADESH	11/2016	215.16 215.00	09/2019 -	-
475	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO - [N24001143]MoRTH,UTTAR PRADESH	10/2016	176.94 177.00	10/2018 -	-
476	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2- - [N24001147]MoRTH,UTTAR PRADESH	10/2016	239.63 -	02/2019 -	-
477	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F - [N24001148]MoRTH,UTTAR PRADESH	03/2016	599.34 -	01/2020 -	-
478	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA	02/2018	355.99 -	12/2019 -	-
479	WARDHA TO ARVI - [N24001150]MoRTH,MAHARASHTRA	02/2018	313.58 -	04/2020 -	-
480	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM - [N24001153]MoRTH,ASSAM	11/2010	197.37 -	02/2014 -	-
481	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT - [N24001154]MoRTH,KARNATAKA	08/2016	367.44 -	01/2017 -	-
482	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT - [N24001155]MoRTH,KARNATAKA	08/2016	175.20 -	01/2017 -	-
483	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS - PA - [N24001156]MoRTH,KARNATAKA	01/2017	166.67 -	09/2017 -	-
484	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA	08/2016	175.50 -	02/2017 -	-
485	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA	03/2018	159.97 -	06/2019 -	-

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
486	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]MoRTH,KARNATAKA	01/2018	159.70 -	07/2018 -	-
487	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA	09/2017	191.60 -	10/2018 -	-
488	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]MoRTH,KARNATAKA	12/2017	297.30 -	01/2019 -	-
489	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA	03/2018	325.86 -	10/2018 -	-
490	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]MoRTH,KARNATAKA	08/2016	329.01 -	02/2017 -	-
491	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA	10/2016	396.96 -	03/2017 -	-
492	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA	11/2016	314.90 -	03/2017 -	-
493	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA	03/2015	159.12 -	01/2016 -	-
494	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776) - [N24001167]MoRTH,KARNATAKA	03/2015	165.67 -	01/2016 -	-
495	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA	05/2018	171.60 -	05/2018 -	-
496	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM. - [N24001170]MoRTH,KARNATAKA	01/2014	471.16 -	08/2014 -	-
497	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA	01/2017	291.49 -	08/2017 -	-
498	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND	11/2016	336.25 369.96	09/2019 11/2020	-
499	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S - [N24001183]MoRTH,ANDHRA PRADESH	07/2014	251.55 -	02/2015 -	-
500	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR	02/2019	2,926.42 -	- -	-
501	REHABILITATION AND UPGRADATION OF BARAICH -SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA - [N24001202]MoRTH,UTTAR PRADESH	03/2016	388.83 -	12/2019 -	-
502	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH,UTTAR PRADESH	03/2018	306.59 -	- -	-

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
503	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH,UTTAR PRADESH	11/2018	281.45 -	- -	-
504	WIDENING OF SL TO 2 L KM. 107-184.80 SUKUMA TO KONTA ON NH 221 - [N24001223]MoRTH,CHANDIGARH	03/2010	179.89 271.00	03/2013 05/2019	-
505	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1 - [N24001225]MoRTH,CHANDIGARH	12/2010	169.26 299.00	01/2019 -	-
506	WIDENING TO 4 LANE / 4 LANE WITH PAVED SHOULDERS WITH STRENGTHENING OF EXISTING CARRIAGEWAY IN KM 0/- [N24001237]MoRTH,TAMIL NADU	01/2016	162.72 -	09/2016 -	-
507	CONSTRUCTION OF FLYOVER FROM KM 604/252 TO 607/060 (MARTHANDAM JUNCTION) AND FROM KM 630/116 TO 631/- [N24001238]MoRTH,TAMIL NADU	05/2016	307.70 -	01/2017 -	-
508	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM - [N24001239]MoRTH,TAMIL NADU	03/2018	240.38 -	06/2019 -	-
509	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W - [N24001243]MoRTH,ASSAM	03/2020	166.94 -	12/2020 -	-
510	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1) - [N24001289]MoRTH,ARUNACHAL PRADESH	03/2019	403.68 -	02/2020 -	-
511	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2 - [N24001290]MoRTH,ARUNACHAL PRADESH	03/2019	342.55 -	02/2020 -	-
512	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE - [N24001291]MoRTH,ARUNACHAL PRADESH	03/2019	421.48 -	11/2020 -	-
513	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE - [N24001292]MoRTH,ARUNACHAL PRADESH	03/2019	543.05 -	11/2020 -	-
514	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE - [N24001293]MoRTH,ARUNACHAL PRADESH	03/2019	486.70 -	10/2020 -	-
515	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE - [N24001294]MoRTH,ARUNACHAL PRADESH	03/2019	560.39 -	02/2020 -	-
516	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE - [N24001295]MoRTH,ARUNACHAL PRADESH	03/2019	347.78 -	09/2020 -	-
517	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG - [N24001296]MoRTH,ARUNACHAL PRADESH	03/2019	394.27 -	10/2020 -	-
518	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE - [N24001297]MoRTH,ARUNACHAL PRADESH	03/2019	450.65 -	11/2020 -	-
519	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 - [N24000895]MoRTH,MADHYA PRADESH	09/2016	287.34 -	01/2019 09/2020	11/2020
520	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH,ARUNACHAL PRADESH	09/2011	1,979.00 -	- 03/2020	-
National Highways And Infrastructure Development Corporation Ltd.					

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
521	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL,ARUNACHAL PRADESH	10/2015	210.50 210.50	- 01/2016	01/2019
522	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND	02/2017	387.00 -	09/2018 -	09/2020
523	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM	05/2015	454.89 -	05/2018 -	12/2020
524	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 -	04/2017 -	02/2021
525	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH	03/2017	284.09 284.09	04/2017 03/2018	03/2021
526	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL,ASSAM	06/2016	829.00 -	01/2019 -	-
527	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM	03/2015	168.39 -	11/2018 -	-
528	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM	10/2014	588.95 -	11/2018 -	-
529	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH	07/2015	197.16 -	10/2018 -	-
530	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH	03/2015	394.00 -	06/2018 -	-
531	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA	10/2014	369.00 -	03/2018 -	-
532	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM	12/2015	223.30 -	06/2018 -	-
533	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-
534	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM	12/2015	289.99 -	12/2018 -	-
535	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM	01/2016	252.00 -	01/2016 -	-
536	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH	04/2016	245.79 -	- -	-
537	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH	04/2016	198.00 -	10/2016 -	-
538	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH	11/2015	434.06 -	- -	-
539	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH	12/2016	138.93 155.00	01/2017 -	-

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
540	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH	02/2017	195.23 -	04/2017 -	-
541	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH	02/2017	203.36 -	04/2017 -	-
542	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH	01/2017	194.66 -	04/2017 -	-
543	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH	02/2017	167.28 -	04/2017 -	-
544	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND	02/2017	507.68 -	04/2017 -	-
545	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH	01/2017	198.22 -	04/2017 -	-
546	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM	04/2017	388.00 -	10/2017 -	-
547	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND	03/2018	274.31 -	05/2018 -	-
548	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND	03/2018	403.36 -	06/2018 -	-
549	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND	03/2018	417.24 -	05/2018 -	-
550	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS	03/2015	262.97 -	10/2018 -	-
551	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS	03/2017	409.85 -	12/2017 -	-
552	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS	03/2015	277.17 -	04/2017 -	-
553	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS	02/2018	391.00 -	10/2018 -	-
554	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS	03/2018	234.27 -	10/2018 -	-
555	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND	03/2018	237.72 -	09/2018 -	-
556	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND	03/2018	251.97 -	09/2018 -	-
557	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND	03/2018	282.98 -	09/2018 -	-

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
558	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA - [N24000766]NHIDCL,SIKKIM	04/2017	318.42 -	11/2017 -	-
559	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM	03/2017	375.80 -	- -	-
560	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM	11/2017	290.05 -	11/2017 -	-
561	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM	03/2018	264.84 -	06/2018 -	-
562	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM	03/2015	829.00 -	01/2016 -	-
563	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL,UTTARAKHAND	03/2018	1,383.78 -	07/2018 -	-
564	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866]NHIDCL,JAMMU AND KASHMIR	03/2018	404.17 -	08/2018 -	-
565	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM - [N24000867]NHIDCL,JAMMU AND KASHMIR	03/2018	216.00 -	11/2018 -	-
566	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR	03/2018	253.44 -	07/2019 -	-
567	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL,ASSAM	10/2017	818.00 -	- -	-
568	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA	03/2019	306.28 -	05/2019 -	-
569	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH	12/2016	200.44 -	- -	-
570	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH	03/2017	1,718.59 -	- -	-
571	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH	09/2016	568.92 -	- -	-
572	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH	12/2016	188.78 -	- -	-
573	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN - [N24000978]NHIDCL,ARUNACHAL PRADESH	03/2015	172.75 -	- -	-
574	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI - [N24000979]NHIDCL,ARUNACHAL PRADESH	01/2017	256.66 -	- -	-
575	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8 - [N24001184]NHIDCL,DELHI	07/2017	269.69 -	09/2019 -	-

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
576	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL,ASSAM	03/2017	1,049.51 -	- -	-
	<u>National Highways Authority Of India</u>				
577	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- -	01/2020
578	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	- -	01/2021
579	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN	09/2016	1,239.82 -	- -	01/2021
580	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	09/2017 -	01/2021
581	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	03/2019 -	02/2021
582	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	07/2016 -	02/2021
583	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 -	03/2021
584	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	03/2021
585	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	06/2018 -	03/2021
586	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	08/2019 -	03/2021
587	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	03/2019 -	03/2021
588	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	- -	08/2020
589	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	10/2017 -	11/2020
590	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	04/2018 -	12/2020
591	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	06/2015
592	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- 06/2015	06/2015
593	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	07/2018
594	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 -	06/2019
595	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	04/2010 -	07/2019
596	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 -	09/2019
597	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	06/2019 -	09/2019

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
598	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI, UTTAR PRADESH	04/2014	495.78 627.93	01/2016 01/2020	01/2020
599	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI, MADHYA PRADESH	03/2015	795.76 686.13	- -	05/2020
600	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI, MADHYA PRADESH	03/2015	794.30 679.94	- -	05/2020
601	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI, RAJASTHAN	11/2012	530.07 -	08/2016 -	06/2020
602	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, ASSAM	12/2003	245.00 -	03/2008 -	08/2020
603	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI, JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	09/2020
604	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI, RAJASTHAN	02/2018	1,103.88 -	- -	09/2020
605	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI-ENNORE PORT CONNECTIVITY - [N24000173]NHAI, TAMIL NADU	06/2011	600.00 -	06/2013 -	10/2020
606	SRINAGAR TO BANIHAI - [N24000189]NHAI, JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	10/2020
607	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI, MAHARASHTRA	12/2017	404.94 -	- -	10/2020
608	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270 (D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI, MAHARASHTRA	09/2015	414.51 -	05/2018 11/2020	11/2020
609	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI, KARNATAKA	03/2016	870.00 -	03/2019 -	11/2020
610	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH	07/2012	291.36 469.31	01/2014 12/2020	12/2020
611	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI, UTTAR PRADESH	04/2014	351.34 417.68	01/2016 12/2020	12/2020
612	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI, KARNATAKA	05/2014	1,655.01 -	08/2016 -	12/2020
613	FOUR LANING OF RAMBAN - BANIHAI SECTION OF NH-1A - [N24000471]NHAI, JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	12/2020
614	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI, KARNATAKA	08/2016	1,664.20 -	04/2020 -	12/2020
615	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI, HARYANA	03/2018	1,484.30 -	- 06/2021	12/2020
616	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI, BIHAR	05/2011	511.54 585.00	11/2013 12/2020	01/2021
617	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI, JAMMU AND KASHMIR	12/2017	1,471.75 1,339.00	- -	01/2021
618	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI, GUJARAT	02/2018	1,052.21 -	- -	01/2021
619	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, ASSAM	12/2003	208.00 -	04/2008 -	02/2021

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
620	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	07/2018 -	02/2021
621	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT	06/2017	1,958.88 -	06/2020 -	02/2021
622	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH	03/2018	565.09 -	- -	02/2021
623	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	03/2021
624	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	11/2018 07/2019	03/2021
625	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	08/2018 -	03/2021
626	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	- -	03/2021
627	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	- -	03/2021
628	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH	03/2018	1,029.96 -	- -	03/2021
629	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	-
630	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	-
631	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	-
632	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-
633	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	-
634	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-
635	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	-
636	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	09/2012 -	-
637	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	08/2011 -	-
638	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	-
639	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	-
640	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	06/2018 -	-
641	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	-

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
642	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-
643	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-
644	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-
645	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-
646	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	-
647	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-
648	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	-
649	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-
650	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	-
651	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	-
652	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-
653	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	-
654	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	-
655	MUZZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	-
656	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	09/2014 -	-
657	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	10/2013 -	-
658	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	06/2015 -	-
659	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-
660	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	12/2015 -	-
661	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	02/2014 -	-
662	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	-
663	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	09/2016 -	-
664	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 -	-
665	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	11/2017 -	-
666	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	12/2017 -	-

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
667	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 -	05/2017 -	-
668	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	-
669	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	-
670	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 -	-
671	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	10/2017 -	-
672	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	05/2019 -	-
673	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI,WEST BENGAL	10/2015	361.15 -	- -	-
674	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	05/2019 -	-
675	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	06/2016 -	-
676	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	04/2018 -	-
677	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 -	07/2018 -	-
678	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	01/2019 -	-
679	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	07/2017 -	-
680	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	-
681	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-
682	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 -	06/2018 -	-
683	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-
684	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	-
685	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 -	03/2018 -	-
686	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	04/2019 -	-
687	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	-
688	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	08/2018 -	-
689	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 -	06/2018 -	-
690	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	-

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
691	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	-
692	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	05/2018 -	-
693	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	-
694	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 -	07/2018 -	-
695	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 -	06/2018 -	-
696	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	04/2018 -	-
697	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 -	12/2017 -	-
698	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	- -	-
699	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	- -	-
700	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 -	01/2018 -	-
701	FOUR LANING FROM MPMHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	-
702	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	- -	-
703	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	05/2018 -	-
704	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	04/2019 -	-
705	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS - DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	- -	-
706	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	- -	-
707	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR	08/2015	516.13 -	04/2018 -	-
708	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-
709	MEERUT-BULANDSHAHAR - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	- -	-
710	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 -	06/2019 -	-
711	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 -	07/2018 -	-
712	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	04/2019 -	-
713	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	11/2018 -	-
714	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	02/2019 -	-

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
715	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-
716	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 -	03/2019 -	-
717	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-
718	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	04/2019 -	-
719	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI, WEST BENGAL	03/2016	229.37 -	11/2018 -	-
720	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	04/2019 -	-
721	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	- -	-
722	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	- -	-
723	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	-
724	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	- -	-
725	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	- -	-
726	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	- -	-
727	FOUR LANING OF TALAJA - MAHUVA SECTION OF NH - 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT	05/2016	834.64 -	- -	-
728	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	- -	-
729	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	- -	-
730	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	-
731	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN	06/2016	763.23 -	06/2019 -	-
732	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	06/2019 -	-
733	BALANCE WORK OF 4 LANING OF GORAKHPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	-
734	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 -	- -	-

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
735	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	-
736	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	10/2018 -	-
737	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	- -	-
738	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	04/2019 -	-
739	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 -	09/2019 -	-
740	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 -	- -	-
741	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH	08/2016	227.49 -	01/2019 -	-
742	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	-
743	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	08/2018 -	-
744	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	05/2019 -	-
745	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-
746	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 -	08/2018 -	-
747	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 -	08/2019 -	-
748	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA	09/2016	1,004.67 -	05/2019 -	-
749	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	- -	-
750	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-
751	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT	12/2016	417.19 -	- -	-
752	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	-
753	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	07/2018 -	-
754	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
755	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	- -	-
756	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	05/2019 -	-
757	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 -	02/2020 -	-
758	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	03/2020 -	-
759	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	03/2020 -	-
760	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA	03/2017	247.02 -	03/2020 -	-
761	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA	03/2017	744.64 -	03/2020 -	-
762	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	03/2020 -	-
763	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	03/2020 -	-
764	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	-
765	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA	03/2017	296.19 -	03/2020 -	-
766	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	03/2020 -	-
767	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	03/2020 -	-
768	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR	03/2017	672.89 -	03/2020 -	-
769	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	-
770	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH	03/2017	2,064.99 -	03/2020 -	-
771	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	03/2020 -	-
772	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	03/2020 -	-
773	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	-
774	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	10/2017 -	-

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
775	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH	09/2017	374.40 -	09/2017 -	-
776	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	-
777	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	- -	-
778	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	- -	-
779	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	- -	-
780	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	- -	-
781	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-
782	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- -	-
783	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-
784	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 -	- -	-
785	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-
786	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-
787	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-
788	FOUR LANING OF DELINKED STRETCH OF SEONI - MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH	01/2018	960.24 -	- -	-
789	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA	01/2018	633.68 -	- -	-
790	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 -	- -	-
791	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA	03/2017	4,429.00 -	03/2017 -	-
792	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA	02/2018	486.78 -	- -	-
793	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 -	- -	-
794	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 -	- -	-

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
795	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 -	- -	-
796	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 -	- -	-
797	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH	03/2018	925.40 -	- -	-
798	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN	02/2018	741.86 -	- -	-
799	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN	02/2018	716.76 -	- -	-
800	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	-
801	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 -	- -	-
802	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH	03/2018	1,025.80 -	- -	-
803	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH	03/2018	1,115.28 -	- -	-
804	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K - [N24000804]NHAI,TELANGANA	03/2018	802.65 -	- -	-
805	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 -	- -	-
806	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-
807	CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	- -	-
808	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	- -	-
809	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA	03/2018	950.63 -	- -	-
810	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA	03/2018	857.62 -	- -	-
811	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI,TELANGANA	03/2018	828.29 -	- -	-
812	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU	03/2018	633.55 -	- -	-

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
813	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU	03/2018	2,065.96 -	- -	-
814	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE	03/2018	1,294.47 -	- -	-
815	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE	03/2018	998.70 -	- -	-
816	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT	03/2018	1,161.39 -	- -	-
817	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA	03/2018	275.12 -	- -	-
818	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXIST - [N24000837]NHAI,HARYANA	03/2018	307.79 -	- -	-
819	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN	03/2018	874.25 -	- -	-
820	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN	03/2018	1,158.35 -	- -	-
821	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB	03/2018	199.90 -	- -	-
822	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB	03/2018	196.05 -	- -	-
823	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA	03/2018	198.05 -	- -	-
824	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA	03/2018	181.78 -	- -	-
825	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA	03/2018	551.58 -	- -	-
826	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA	03/2018	642.13 -	- -	-
827	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 -	- -	-
828	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - [N24001185]NHAI,UTTAR PRADESH	11/2017	2,159.00 -	01/2019 -	-
829	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI,HARYANA	01/2019	1,051.91 -	- -	-
830	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI,HARYANA	01/2019	1,120.06 -	- -	-

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
831	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA	01/2019	1,137.42 -	- -	-
832	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA	01/2019	1,033.19 -	- -	-
833	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA	01/2019	1,243.45 -	- -	-
834	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA	01/2019	889.36 -	- -	-
835	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA	01/2019	1,018.79 -	- -	-
836	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA	01/2019	996.65 -	- -	-
837	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214]NHAI,MADHYA PRADESH	12/2017	217.96 -	- -	-
838	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T - [N24001234]NHAI,MADHYA PRADESH	02/2019	996.27 -	03/2020 -	-
839	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105 - [N24001298]NHAI,ANDHRA PRADESH	09/2018	597.67 -	01/2020 -	-
840	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN - [N24001299]NHAI,ANDHRA PRADESH	09/2018	617.41 -	02/2019 -	-
841	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300]NHAI,ANDHRA PRADESH	11/2019	1,226.88 -	02/2021 -	-
842	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - [N24001301]NHAI,ANDHRA PRADESH	11/2019	1,601.10 -	02/2021 -	-
843	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT - [N24001303]NHAI,BIHAR	10/2013	649.90 -	12/2020 -	-
844	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE - [N24001304]NHAI,BIHAR	10/2013	446.97 -	11/2020 -	-
845	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA - [N24001305]NHAI,BIHAR	10/2013	464.09 -	11/2020 -	-
846	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	-
	Total		4,03,696.02 -		
	<u>URBAN DEVELOPMENT</u>				
	<u>Central Public Works Department</u>				
847	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	12/2015 -	-
848	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	12/2013 -	-

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
849	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD,DELHI	11/2017	238.56 -	05/2020 -	-
850	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI - [N28000123]CPWD,DELHI	07/2017	218.72 -	11/2020 -	-
851	C/O STEEL STRUCTURE BUILDINGS USING PRE-ENGINEERED TECHNOLOGY AT AFRICA AVENUE AND KG MARG - [N28000143]CPWD,DELHI	02/2020	532.00 -	11/2020 -	-
852	CONSTRUCTION 729 QUARTERS (TYPE II-180, TYPE III-364, TYPE IV-112, TYPE V-68, TYPE VI-5), SHOPS, CO - [N28000149]CPWD, CHHATISGARH	05/2019	299.97 -	09/2020 -	-
	<u>Chennai Metro Rail Ltd</u>				
853	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL, TAMIL NADU	06/2016	3,770.00 -	03/2018 -	03/2021
854	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL, TAMIL NADU	02/2009	14,600.00 -	12/2015 -	-
	<u>Kochi Metro Rail Corporation Ltd</u>				
855	KOCHI METRO RAIL PROJECT - [N28000081]KMRL, KERALA	07/2012	5,181.79 -	07/2017 -	09/2020
	<u>Lucknow Metro Rail Corporation Limited</u>				
856	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRL, UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	-
	<u>Nagpur Metro Rail Corporation Ltd</u>				
857	NAGPUR METRO RAIL - [N28000085]NMRL, MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	-
	<u>National Building Construcion Corporation Ltd</u>				
858	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC, DELHI	06/2012	4,264.00 -	11/2019 -	-
	Total		45,711.60 -		
	<u>WATER RESOURCES</u>				
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>				
859	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]BUIDCO, BIHAR	12/2014	225.77 -	03/2020 -	03/2021
860	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO, BIHAR	10/2017	254.13 -	09/2020 -	-
861	SAIDPUR SEWER NETWORK PATNA - [N30000039]BUIDCO, BIHAR	04/2015	268.63 -	01/2021 -	-
862	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]BUIDCO, BIHAR	05/2017	191.62 -	11/2020 03/2021	-
	<u>Delhi Jal Board</u>				
863	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018]DJB, DELHI	05/2017	344.81 -	05/2020 -	-
	<u>Hindustan Steelwork Construction Limited</u>				
864	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL, BIHAR	10/2005	956.00 -	03/2015 -	-
	<u>Kolkata Metropolitan Development Authority</u>				

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
865	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]KMDA, WEST BENGAL	12/2014	272.32 -	04/2020 -	03/2021
	<u>Uttar Pradesh Jal Nigam</u>				
866	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020]UPJalNigam, UTTAR PRADESH	02/2011	279.91 330.05	12/2019 -	01/2021
867	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA - [N30000011]UPJalNigam, UTTAR PRADESH	02/2017	161.31 -	11/2019 -	03/2021
868	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR - [N30000009]UPJalNigam, UTTAR PRADESH	10/2016	370.40 430.49	08/2020 03/2021	-
	<u>Uttarakhand Pey Jal Nigam</u>				
869	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI - [N30000003]UKJalNigam, UTTARAKHAND	03/2017	273.37 -	08/2019 -	-
870	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH - [N30000004]UKJalNigam, UTTARAKHAND	03/2017	158.00 -	11/2019 03/2021	-
	Total		3,756.27 -		
	<u>COMMERCE</u>				
	<u>National Building Construcion Corporation Ltd</u>				
871	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI - [N40000003]NBCC, DELHI	06/2018	302.64 -	10/2020 -	-
	Total		302.64 -		
	<u>HUMAN RESOURCE DEVELOPMENT</u>				
	<u>Central Public Works Department</u>				
872	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD, HIMACHAL PRADESH	11/2012	270.83 -	11/2014 -	-
873	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD, KERALA	01/2010	165.23 -	10/2012 -	-
874	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD, RAJASTHAN	12/2016	549.31 -	07/2019 -	-
875	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133]CPWD, ANDHRA PRADESH	02/2019	186.00 199.00	09/2020 -	-
876	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED - [N28000146]CPWD, WEST BENGAL	03/2020	193.83 -	06/2020 -	-
877	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA. - [N42000002]CPWD, GOA	05/2019	303.90 -	03/2020 -	-
878	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE - [N42000005]CPWD, ANDHRA PRADESH	02/2019	655.34 -	06/2020 -	-
	<u>Edcil(India) Limited</u>				
879	STUDY IN INDIA - [N42000003]EDCIL, MULTI STATE	03/2018	150.00 -	04/2018 -	-
	<u>Indian Institute Of Technology, Kharagpur</u>				
880	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION - [N42000004]IITKGP, MULTI STATE	08/2018	418.00 -	03/2019 -	-

Costing Rs. 150 Crore and above					(April 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>Rail India Technical And Economic Service</u>				
881	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]RITES,MEGHALAYA	09/2013	484.32 -	09/2014 -	-
	Total		3,376.76 -		
	<u>CULTURE DEVELOPMENT</u>				
	<u>Hindustan Steelwork Construction Limited</u>				
882	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGHALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	09/2017 -	03/2021
	Total		151.33 -		
	Grand Total		6,75,874.83		

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2021)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
	<u>Bhavini Limited</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 5,677.00	6,840.00	5,935.96	09/2010 09/2016	10/2022	145	73
	<u>Nuclear Power Corporation Of India Limited</u>								
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	16,580.00	16,488.00	12/2015 -	02/2022	74	-
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	17,079.00	13,206.00	12/2016 -	03/2023	75	-
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL,TAMIL NADU	03/2013	39,849.00 -	39,849.00	23,925.00	11/2020 -	11/2023	36	-
	Total		67,120.00 -	80,348.00	59,554.96				
	<u>CIVIL AVIATION</u>								
	<u>Airport Authority Of India Limited</u>								
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,A & N ISLANDS	10/2013	417.23 707.73	707.73	379.95	09/2018 09/2020	06/2021	33	9
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI,TRIPURA	09/2015	438.28 -	402.00	366.61	06/2019 12/2020	06/2021	24	6
7	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN - [N04000085]AAI,UTTARAKHAND	07/2018	456.86 -	456.86	286.85	09/2020 -	12/2021	15	-
8	UPGRADATION OF JABALPUR AIRPORT - [N04000087]AAI,MADHYA PRADESH	06/2016	412.24 -	412.24	195.70	06/2021 -	12/2021	6	-
9	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT - [N04000089]AAI,ANDHRA PRADESH	08/2017	177.10 -	177.10	86.01	02/2020 06/2021	12/2021	22	6
10	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076]AAI,DELHI	11/2016	303.80 351.21	303.80	167.55	04/2020 -	03/2022	23	-
11	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]AAI,TAMIL NADU	08/2018	951.28 -	951.28	408.94	10/2021 -	07/2022	9	-
12	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI - [N04000074]AAI,TAMIL NADU	06/2018	2,467.00 -	2,467.00	608.22	02/2022 -	08/2022	6	-
13	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]AAI,UTTAR PRADESH	06/2018	1,383.00 -	1,383.00	369.66	09/2021 -	09/2022	12	-
14	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082]AAI,BIHAR	05/2018	1,216.90 -	1,216.90	205.04	10/2022 -	03/2023	5	-

Costing Rs. 150 Crore and above

(April 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
15	DEVELOPMENT OF TUTICORIN AIRPORT - [N04000090]AAI,TAMIL NADU	06/2019	380.87 -	380.87	5.99	03/2022 03/2022	03/2023	12	12
	Total		8,604.56 -	8,858.78	3,080.52				
	<u>COAL</u>								
	<u>Bharat Coking Coal Limited</u>								
16	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	289.45	281.33	05/2014 -	07/2021	86	-
17	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	463.92	04/2015 -	03/2022	83	-
18	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]BCCL, WEST BENGAL	12/2015	304.13 341.22	341.22	40.84	03/2017 -	03/2022	60	-
19	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]BCCL,JHARKHAND	10/2015	243.00 334.27	334.27	18.35	04/2018 -	06/2022	50	-
20	MURAIIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	24.23	04/2014 -	04/2023	108	-
	<u>Central Coal Fields Limited</u>								
21	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	107.27	03/2011 -	03/2022	132	-
22	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	426.30	03/2016 -	03/2022	72	-
23	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	98.21	03/2014 -	03/2022	96	-
	<u>Eastern Coal Fields Limited</u>								
24	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL, WEST BENGAL	08/2012	1,055.05 -	1,055.05	669.82	03/2018 -	10/2021	43	-
	<u>Mahanadi Coal Fields Limited</u>								
25	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	479.53	475.14	03/2013 -	03/2022	108	-
26	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA	05/2014	479.15 -	479.15	278.53	03/2019 -	03/2024	60	-
27	GARJANBAHAL OCP - [N06000117]MCL,ODISHA	11/2014	1,375.38 -	1,375.38	504.36	03/2021 -	03/2024	36	-
28	BHUBANESWARI EXPENSION OCP(40.0 MTY) - [N06000034]MCL,ODISHA	12/2007	3,145.45 -	3,145.45	612.55	03/2017 -	03/2031	168	-
	<u>Neyveli Lignite Corporation</u>								
29	PACHWARA SOUTH COAL BLOCK - [N06000193]NLC,JHARKHAND	07/2013	1,795.01 -	1,795.01	34.88	08/2022 -	09/2023	13	-
	<u>Northern Coal Fields Limited</u>								
30	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL,MADHYA PRADESH	05/2017	1,783.09 -	1,783.09	622.66	03/2021 -	03/2022	12	-
31	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]NCL,MADHYA PRADESH	11/2017	1,255.17 -	1,255.17	152.16	03/2022 -	03/2023	12	-
	<u>Singareni Colliers Company Limited</u>								
32	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	164.04	129.58	03/2015 -	03/2022	84	-
33	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	349.28	251.14	03/2015 -	03/2022	84	-
34	KALYANIKHANI OPENCASE PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	384.32	131.62	07/2016 -	03/2022	68	-

Costing Rs. 150 Crore and above

(April 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
35	KAKATIYAKHANI OPENCAS-2 PROJECT - [N06000129]SCCL,TELANGANA	05/2015	397.09 -	442.42	109.25	03/2019 -	03/2022	36	-
36	KAKATIYAKHANI OPENCAS III PROJECT PHASE-1 - [N06000161]SCCL,TELANGANA	03/2017	413.84 -	413.84	230.95	03/2019 -	03/2022	36	-
37	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	489.62	416.07	03/2012 -	03/2023	132	-
38	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	473.22	79.04	03/2015 -	03/2023	96	-
	<u>South-Eastern Coal Fields Limited</u>								
39	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH	09/2008	152.43 459.49	459.49	202.90	03/2015 03/2020	03/2022	84	24
40	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	6.50	03/2014 -	03/2022	96	-
41	AMADAND OPENCAS EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH	03/2016	869.44 -	869.44	123.17	03/2021 -	03/2022	12	-
42	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL,CHHATISGARH	06/2010	11,816.40 -	11,816.40	4,487.05	03/2023 03/2016	03/2023	0	84
43	AMERA OC RCE - [N06000123]SECL,CHHATISGARH	02/2015	335.97 -	335.97	49.49	03/2018 -	03/2023	60	-
44	AMGAON OPENCAS PROJECT RCE - [N06000135]SECL,CHHATISGARH	07/2015	316.10 -	316.10	141.02	03/2020 -	03/2023	36	-
45	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH	12/2014	371.04 -	371.04	77.27	03/2021 -	03/2024	36	-
46	DURGAPUR OPENCAS PROJECT - [N06000136]SECL,CHHATISGARH	02/2015	916.24 -	916.24	11.38	03/2023 -	03/2026	36	-
	<u>Western Coal Fields Limited</u>								
47	SINGHORI OC MINE - [N06000130]WCL,MAHARASHTRA	06/2015	205.49 -	205.49	138.12	03/2020 -	09/2021	18	-
48	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL,MAHARASHTRA	02/2016	198.68 -	325.18	253.17	03/2019 -	03/2022	36	-
49	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL,MAHARASHTRA	03/2017	362.73 -	402.90	330.34	03/2020 -	09/2022	30	-
50	UKNI DEEP OC - [N06000179]WCL,MAHARASHTRA	11/2018	318.14 -	318.14	211.41	03/2021 -	09/2022	18	-
51	BELLORA-NAIGAON DEEP OC - [N06000180]WCL,MAHARASHTRA	11/2018	252.71 -	252.71	101.09	03/2021 -	09/2022	18	-
52	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL,MULTI STATE	02/2017	328.00 -	328.00	295.83	03/2021 -	09/2023	30	-
53	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA	08/2015	288.90 -	333.43	142.27	03/2023 -	03/2024	12	-
54	REVISED PR FOR AMALGAMATED INDER KAMPTEE DEEP OC (3.2 MTY) - [N06000141]WCL,MAHARASHTRA	11/2015	313.34 -	313.34	148.72	03/2021 -	03/2024	36	-
55	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]WCL,MULTI STATE	09/2016	289.29 -	289.30	35.95	03/2022 -	03/2025	36	-
56	RPR FOR MUNGOLI NIORGUDA EXTENSION (DEEP) OC (4.375 MTY) - [N06000142]WCL,MAHARASHTRA	11/2015	851.60 -	826.80	230.50	03/2020 -	03/2026	72	-
57	RPR FOR JAMUNIA UG (0.90 MTY) - [N06000153]WCL,MADHYA PRADESH	07/2016	281.25 -	281.25	21.35	03/2022 -	03/2026	48	-
58	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA	05/2015	295.56 -	496.38	164.25	03/2019 -	09/2026	90	-

Costing Rs. 150 Crore and above

(April 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
59	BHATADI EXPANSION OC MINE - [N06000150]WCL, MAHARASHTRA	02/2016	304.52 -	729.86	160.67	03/2019 -	09/2026	90	-
60	PR FOR DINESH(MAKARDHOKRA III) EXPANSION OC (8.0 MTY) - [N06000118]WCL, MAHARASHTRA	11/2014	1,184.33 -	1,184.33	383.13	03/2020 -	03/2027	84	-
	Total		37,541.32 -	39,006.71	13,873.78				
	<u>FINANCE</u>								
	<u>Central Public Works Department</u>								
61	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD, TAMIL NADU	12/2015	209.00 -	208.96	205.72	10/2019 -	07/2021	21	-
	Total		209.00 -	208.96	205.72				
	<u>FERTILISERS</u>								
	<u>Rashtriya Chemical & Fertiliser Limited</u>								
62	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]RCF, MAHARASHTRA	04/2018	426.72 -	426.72	288.80	04/2020 03/2021	07/2021	15	4
	Total		426.72 -	426.72	288.80				
	<u>STEEL</u>								
	<u>Steel Authority Of India Limited (Sail)</u>								
63	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL, JHARKHAND	11/2016	262.87 -	262.87	185.85	06/2019 05/2021	08/2021	26	3
64	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E - [N12000121]SAIL, WEST BENGAL	12/2018	263.36 -	263.36	215.38	09/2020 03/2021	09/2021	12	6
	Total		526.23 -	526.23	401.23				
	<u>PETROLEUM</u>								
	<u>Bharat Petroleum Corporation Limited</u>								
65	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT (PDPP) AT KOCHI REFINERY - [N16000227]BPCL, KERALA	11/2014	4,588.29 5,245.96	5,245.96	5,076.00	08/2018 11/2019	05/2021	33	18
66	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL, KERALA	02/2016	3,313.00 -	3,288.96	2,967.01	02/2020 03/2021	05/2021	15	2
67	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]BPCL, KARNATAKA	10/2018	206.26 -	206.26	132.84	03/2021 -	05/2021	2	-
68	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL, KERALA	12/2015	1,112.00 1,507.24	1,507.24	730.00	06/2019 -	02/2022	32	-
69	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364]BPCL, ANDHRA PRADESH	07/2017	580.20 -	580.20	155.84	02/2021 -	03/2023	25	-

Costing Rs. 150 Crore and above

(April 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>Chennai Petroleum Corporation Limited</u>								
70	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU	08/2017	421.00 -	300.00	241.01	08/2020 -	09/2021	13	-
	<u>Gas Authority Of India Limited</u>								
71	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT	04/2016	327.78 -	200.00	196.50	04/2018 -	06/2021	38	-
72	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]GAIL,HARYANA	08/2018	286.42 327.01	327.01	186.00	08/2020 05/2021	06/2021	10	1
73	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE	07/2015	2,881.40 -	2,000.00	1,607.70	12/2020 -	09/2021	9	-
74	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT - [N16000390]GAIL,UTTAR PRADESH	08/2018	217.92 217.92	217.92	89.80	04/2021 -	10/2021	6	-
75	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]GAIL,GUJARAT	09/2018	225.54 247.90	247.90	40.10	02/2021 -	12/2021	10	-
	<u>Hindustan Petroleum Corporation Limited</u>								
76	SWRO II WITH LLPH FACILITIES - [N16000378]HPCL,ANDHRA PRADESH	09/2019	196.26 -	196.26	92.38	07/2020 -	07/2021	12	-
	<u>Indian Oil Corporation Limited</u>								
77	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00 -	212.00	148.29	01/2021 -	09/2021	8	-
78	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELI - [N16000276]IOCL,MAHARASHTRA	05/2016	261.00 -	261.00	158.24	01/2021 -	09/2021	8	-
79	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 -	348.00	217.55	01/2021 -	10/2021	9	-
80	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	318.80	147.52	08/2021 -	11/2021	3	-
81	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]IOCL,ODISHA	10/2018	1,297.50 -	1,297.50	722.93	10/2021 -	03/2022	5	-
82	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	355.00	106.53	04/2022 -	02/2023	10	-
83	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA	12/2018	611.00 -	611.00	76.47	04/2022 -	08/2023	16	-
	<u>Mangalore Refinery And Petrochemicals Limited</u>								
84	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA	11/2017	581.00 637.00	637.00	489.10	03/2020 11/2020	07/2021	16	8
85	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA	09/2016	1,810.00 1,810.00	1,810.00	1,658.31	12/2019 04/2021	02/2022	26	10
	<u>Oil India Limited</u>								

Costing Rs. 150 Crore and above

(April 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
86	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL, ASSAM	01/2018	543.91 -	652.10	320.30	02/2020 -	06/2021	16	-
87	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN - [N16000356]OIL, ASSAM	06/2016	224.75 -	222.21	166.48	08/2020 -	06/2021	10	-
88	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL, MULTI STATE	09/2016	571.66 -	571.66	471.81	12/2019 -	08/2021	20	-
89	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL, MULTI STATE	05/2016	406.00 -	406.00	225.67	10/2020 -	03/2022	17	-
	Total		21,896.69 -	22,019.98	16,424.38				
	<u>POWER</u>								
	<u>Central Public Works Department</u>								
90	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD, DELHI	10/2017	271.90 -	271.90	240.96	11/2019 -	06/2021	19	-
	<u>Chenab Valley Power Projects [P] Limited</u>								
91	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL, JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	1,766.91	04/2020 -	07/2025	63	-
	<u>National Thermal Power Corporation</u>								
92	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP - [N18000274]NTPC, UTTAR PRADESH	03/2019	349.00 -	349.00	226.00	11/2020 -	04/2021	5	-
93	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC, BIHAR	01/2007	5,353.00 10,566.00	10,566.00	8,847.06	07/2012 06/2020	07/2021	108	13
94	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC, ODISHA	05/2016	1,885.13 -	1,885.13	1,763.69	12/2018 -	07/2021	31	-
95	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC, WEST BENGAL	12/2016	529.68 -	529.68	418.49	11/2018 -	07/2021	32	-
96	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC, BIHAR	01/2013	12,964.60 17,304.00	17,304.00	15,787.92	05/2018 -	12/2021	43	-
97	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC, UTTARAKHAND	11/2006	2,978.48 5,867.38	5,867.38	4,913.02	03/2013 12/2021	12/2022	117	12
98	PATRATU STPP-I (3X800MW) - [N18000275]NTPC, JHARKHAND	11/2017	18,668.00 -	17,112.00	4,351.86	03/2023 -	09/2024	18	-
	<u>Power Grid Corporation Of India Limited</u>								
99	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL, MULTI STATE	03/2016	808.63 -	808.63	662.19	01/2018 04/2021	05/2021	40	1
100	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL, WEST BENGAL	04/2016	454.11 -	454.11	343.81	04/2018 03/2021	05/2021	37	2
101	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL, MULTI STATE	01/2014	374.63 -	374.63	246.80	04/2016 12/2017	06/2021	62	42

Costing Rs. 150 Crore and above

(April 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
102	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	197.40	90.05	03/2018 -	06/2021	39	-
103	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE	05/2016	14,733.37 -	14,733.37	11,552.37	11/2019 04/2021	06/2021	19	2
104	EASTERN REGION STRENGTHENING SCHEME- XVIII - [N18000258]PGCIL,MULTI STATE	03/2017	3,500.00 3,500.00	3,994.00	2,917.31	07/2020 12/2020	06/2021	11	6
105	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 219.66	219.66	157.20	07/2019 04/2021	06/2021	23	2
106	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE	02/2017	322.30 -	322.30	201.55	02/2019 06/2021	09/2021	31	3
107	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE	03/2017	379.95 -	379.95	232.02	12/2019 06/2021	09/2021	21	3
108	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 6,700.00	6,700.00	2,767.14	12/2018 -	12/2021	36	-
109	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 9,129.32	9,129.32	2,163.30	12/2018 -	03/2024	63	-
	<u>Thdc India Limited</u>								
110	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	3,860.35	2,223.06	06/2013 -	12/2023	126	-
111	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH	03/2019	11,089.42 -	11,089.42	1,767.11	09/2023 -	08/2024	11	-
	Total		95,515.22 -	1,14,260.35	63,639.82				
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Central Public Works Department</u>								
112	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA	10/2016	209.84 -	209.84	136.48	03/2020 -	05/2021	14	-
113	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST - [N28000112]CPWD,KERALA	09/2017	150.29 -	150.29	43.43	03/2020 -	12/2021	21	-
114	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT - [N28000139]CPWD,PONDICHERRY	03/2018	195.00 -	195.00	16.41	09/2020 -	04/2022	19	-
115	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD,HIMACHAL PRADESH	12/2018	260.00 -	260.00	25.38	06/2021 -	05/2022	11	-
	<u>Hill Infra Tech Services Limited</u>								

Costing Rs. 150 Crore and above

(April 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
116	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	715.06	548.39	04/2020 -	07/2021	15	-
117	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	557.48	469.13	06/2020 -	07/2021	13	-
118	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 -	747.80	331.55	05/2021 -	07/2022	14	-
	<u>Hospital Services Consultancy Corporation Ltd</u>								
119	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	499.23	494.72	11/2013 -	05/2021	90	-
120	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC, WEST BENGAL	08/2017	355.15 -	355.15	298.76	03/2019 -	06/2021	27	-
121	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	363.99	239.89	05/2018 -	12/2021	43	-
	Total		4,311.38 -	4,053.84	2,604.14				
	<u>RAILWAYS</u>								
	<u>Central Railways</u>								
122	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50 -	4,517.49	2,648.51	03/2021 -	03/2023	24	-
123	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89 -	1,377.48	335.23	03/2021 -	03/2023	24	-
124	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19 -	1,283.49	408.70	03/2022 -	03/2023	12	-
125	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02 -	540.02	272.55	03/2022 -	03/2024	24	-
126	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,449.91 -	2,449.91	332.19	03/2023 -	03/2024	12	-
127	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 -	1,035.16	244.12	03/2022 -	03/2024	24	-
128	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 -	637.95	182.65	03/2023 -	03/2024	12	-
	<u>East Central Railways</u>								
129	HAJIPUR - BACHAWARA - [N22000334]JECR,MULTI STATE	05/2015	678.54 678.54	929.86	848.39	03/2019 -	05/2021	26	-
130	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]JECR,BIHAR	04/1996	477.88 283.95	751.55	694.88	03/2012 -	07/2021	112	-
131	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]JECR,UTTAR PRADESH	08/2015	528.57 -	528.57	179.78	03/2019 -	03/2022	36	-
132	GARHWA ROAD-RAMNA - [N22000465]JECR,JHARKHAND	03/2015	348.23 -	348.23	336.32	03/2021 -	03/2022	12	-
133	MUZAFFARPUR SAGALI DOUBLING 100.60 KM - [N22000473]JECR,BIHAR	04/2016	731.64 -	1,185.73	217.95	03/2021 -	06/2022	15	-
134	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]JECR,BIHAR	04/1997	324.73 -	1,070.00	1,069.58	03/2012 -	11/2022	128	-
135	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]JECR,BIHAR	04/2009	548.00 -	819.01	535.44	03/2020 -	03/2023	36	-

Costing Rs. 150 Crore and above

(April 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
136	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR	12/2015	1,200.20 1,200.20	1,200.20	578.18	03/2020 -	03/2023	36	-
137	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR	12/2015	1,491.47 -	1,491.47	508.88	03/2020 -	03/2023	36	-
138	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	1,138.31	03/2020 -	03/2024	48	-
139	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 -	1,215.54	426.72	03/2021 -	03/2024	36	-
	<u>East Coast Railway</u>								
140	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 -	1,539.28	1,109.06	02/2019 -	12/2021	34	-
141	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 238.03	238.03	221.48	03/2020 03/2021	03/2022	24	12
142	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	810.02	171.45	11/2018 -	03/2024	64	-
	<u>Eastern Railways</u>								
143	DEOGHAR - SULTANGANJ (INL), ER - [220100273]JER,MULTI STATE	04/2000	607.09 -	1,425.44	638.05	02/2013 -	03/2024	133	-
144	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]JER,WEST BENGAL	04/2000	1,188.91 -	1,619.48	905.06	03/2019 12/2009	03/2025	72	183
145	BARDHAMAN-KATWA (GC) - [N22000091]JER,WEST BENGAL	04/2007	1,106.62 -	1,091.59	990.33	12/2010 -	03/2025	171	-
146	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]JER,MULTI STATE	04/1987	406.99 -	545.70	149.31	03/2006 -	03/2025	228	-
147	PIRPAINTI-JASIDIH - [N22000219]JER,MULTI STATE	04/2013	915.98 -	2,137.81	388.53	03/2022 -	03/2025	36	-
148	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]JER,MULTI STATE	04/2001	923.52 -	995.10	645.97	03/2016 -	03/2025	108	-
149	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]JER,MULTI STATE	04/2005	595.51 -	769.40	103.86	03/2017 -	03/2025	96	-
150	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]JER,MULTI STATE	04/2010	277.28 -	266.32	191.22	03/2016 -	03/2025	108	-
151	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]JER,MULTI STATE	04/2010	365.17 -	439.30	411.65	03/2017 -	03/2025	96	-
152	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]JER,MULTI STATE	04/2010	494.54 -	494.59	32.00	03/2005 -	03/2025	240	-
153	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAPUR-KRISHNACHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]JER,MULTI STATE	04/2009	499.96 -	680.68	164.09	02/2012 -	03/2025	157	-

Costing Rs. 150 Crore and above

(April 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
154	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	257.42	107.35	03/2014 -	03/2025	132	-
155	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	108	-
	<u>Indian Railway Construction Company Limited</u>								
156	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON,CHHATISGARH	04/2013	3,055.00 -	3,055.15	2,431.72	09/2018 -	03/2022	42	-
157	GEVRA ROAD PENDRA ROAD - [N22000488]IRCON,CHHATISGARH	02/2014	2,288.00 -	4,970.11	866.16	03/2022 -	12/2023	21	-
158	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA	04/2016	5,200.00 -	962.00	54.75	03/2020 -	03/2024	48	-
	<u>Metropolitan Rapid Transport Projects</u>								
159	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	06/2021	63	-
160	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 -	2,980.41	1,768.25	03/2004 -	03/2022	216	-
	<u>North Central Railway</u>								
161	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	2,912.96 -	3,845.60	148.26	03/2022 -	12/2024	33	-
	<u>North East Frontier Railway</u>								
162	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	1,180.19 2,531.34	4,541.38	3,804.55	12/2008 -	05/2021	149	-
163	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM	04/2015	870.96 -	1,873.21	1,309.41	03/2021 -	05/2021	2	-
164	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	569.63 -	742.00	200.28	03/2020 -	03/2022	24	-
165	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	385.20 -	1,043.00	837.67	03/2019 -	03/2023	48	-
166	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	2,393.47 5,021.45	5,521.45	3,954.28	03/2014 -	03/2023	108	-
167	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32 -	2,950.00	1,620.12	03/2022 -	03/2023	12	-
168	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	4,454.17 -	12,264.15	10,994.55	03/2011 -	12/2023	153	-
169	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 2,132.03	2,145.00	1,001.65	03/2019 -	03/2024	60	-
170	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 2,042.51	2,042.51	136.41	03/2019 -	03/2024	60	-
171	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52 -	6,911.00	1,204.64	03/2015 -	12/2024	117	-
	<u>North Eastern Railway</u>								

Costing Rs. 150 Crore and above

(April 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
172	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	1,028.95	172.26	12/2019 -	04/2021	16	-
173	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	213.35	12.86	04/2016 -	12/2021	68	-
174	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	477.31	378.98	01/2019 -	02/2022	37	-
175	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]NER,UTTAR PRADESH	04/2016	600.00 -	366.71	117.64	01/2022 -	03/2022	2	-
176	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	276.90	-	04/2017 -	04/2022	60	-
177	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	150.00	-	04/2017 -	10/2022	66	-
178	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH	04/2016	1,900.00 -	1,277.06	-	01/2022 -	03/2025	38	-
	<u>North Western Railway</u>								
179	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	420.18 -	480.00	357.41	03/2020 -	06/2021	15	-
180	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	860.41	709.62	02/2019 -	06/2022	40	-
181	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	701.81	236.13	03/2020 -	10/2022	31	-
182	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	808.85	232.42	08/2022 -	11/2022	3	-
	<u>Northern Railway</u>								
183	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	893.45	705.53	12/2011 -	06/2021	114	-
184	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 -	859.00	852.73	03/2016 -	06/2021	63	-
185	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 -	27,949.00	24,040.61	11/2002 -	12/2022	241	-
186	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	2,200.00	714.78	07/2012 -	03/2024	140	-
187	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI - [N22000502]NR,PUNJAB	06/2009	404.00 -	404.00	226.25	08/2016 -	08/2025	108	-
	<u>Rail India Technical And Economic Service</u>								
188	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498]RITES,CHHATISGARH	02/2016	393.98 -	393.98	350.81	03/2020 -	06/2021	15	-
	<u>Rail Vikas Nigam Ltd.</u>								
189	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	950.00	810.96	03/2016 -	12/2021	69	-
190	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	713.48 -	2,725.00	2,554.71	03/2020 -	12/2021	21	-
191	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	948.04 -	2,009.00	1,875.48	03/2020 -	12/2021	21	-

Costing Rs. 150 Crore and above

(April 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
192	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	1,402.02 -	1,300.00	1,294.72	03/2020 -	12/2021	21	-
193	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH	04/2011	1,485.85 -	1,835.83	1,571.35	12/2020 -	12/2021	12	-
194	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,548.66 -	1,868.89	1,831.45	12/2021 -	03/2022	3	-
195	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	3,377.00	2,683.67	03/2020 -	03/2022	24	-
196	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70 -	2,440.53	1,337.54	02/2015 -	06/2022	88	-
197	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	1,400.00	1,331.76	03/2019 -	06/2022	39	-
198	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	1,536.00	1,089.84	03/2019 -	06/2022	39	-
199	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	1,825.00	1,411.49	12/2020 -	12/2022	24	-
200	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60 -	1,000.00	688.03	03/2022 -	12/2024	33	-
201	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92 -	1,765.92	887.48	03/2023 -	12/2024	21	-
202	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	4,259.48	2,734.83	03/2016 -	03/2025	108	-
203	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	4,639.00	1,119.31	03/2016 -	03/2025	108	-
204	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00 -	22,716.11	2,997.71	12/2024 -	03/2025	3	-
205	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	2,733.86	40.46	03/2014 -	12/2025	141	-
206	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA	01/1991	2,335.67 -	3,327.72	1,317.36	12/2024 -	12/2026	24	-
<u>South Central Railway</u>									
207	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA	04/2017	119.73 185.00	449.39	7.09	03/2022 -	12/2022	9	-
208	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 1.00	3,421.35	1,895.77	03/2000 -	03/2023	276	-
209	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 -	2,120.16	883.52	03/2009 -	03/2024	180	-
210	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	1,160.48 -	1,160.48	502.93	03/2010 -	03/2024	168	-
211	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 -	1,952.68	567.51	03/2023 -	03/2024	12	-

Costing Rs. 150 Crore and above

(April 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
212	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	2,288.70 -	2,643.25	1,231.85	03/2021 -	03/2024	36	-
213	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	2,063.03	1,416.78	03/2021 -	03/2024	36	-
214	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	3,887.48	1,144.64	03/2022 -	03/2024	24	-
215	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,132.77 -	3,037.95	350.54	03/2014 -	03/2027	156	-
	<u>South East Central Railway</u>								
216	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	511.86 -	2,005.25	1,777.22	04/2020 -	04/2021	12	-
217	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH	04/2010	585.93 -	1,268.32	941.56	02/2019 -	12/2021	34	-
218	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA	09/2016	1,908.51 -	3,524.81	982.38	03/2023 -	12/2023	9	-
219	JHARSUGUDA-BILASPU 4TH LINE - [N22000484]SECR,CHHATISGARH	04/2015	1,973.00 -	2,135.34	351.35	03/2021 -	12/2023	33	-
220	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH	04/2015	1,370.00 -	1,370.94	470.49	12/2021 -	12/2023	24	-
221	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA	06/2018	229.00 -	1,096.00	39.79	12/2021 -	12/2024	36	-
	<u>South Eastern Railway</u>								
222	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 358.68	358.68	314.33	12/2018 12/2018	04/2021	28	28
223	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 1,312.96	1,312.96	940.00	03/2020 03/2020	12/2021	21	21
224	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	1,724.20	839.51	03/2021 03/2021	12/2023	33	33
225	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	651.00 -	1,009.00	7.96	03/2015 -	03/2025	120	-
226	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 1,966.70	2,373.00	485.04	03/2003 -	03/2030	324	-
	<u>South Western Railway</u>								
227	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	1,147.00	911.86	03/2020 -	06/2021	15	-
228	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	986.30 -	986.30	312.23	03/2016 -	12/2023	93	-
229	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 -	279.54	35.29	03/2016 -	12/2023	93	-
230	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 -	1,382.78	7.35	03/2002 -	03/2024	264	-
231	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	832.47	.94	03/2016 -	03/2024	96	-
232	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 -	2,841.84	304.83	12/2018 -	06/2025	78	-
	<u>Southern Railway</u>								
233	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	950.00	928.36	03/2005 -	09/2021	198	-

Costing Rs. 150 Crore and above

(April 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
234	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU	02/2015	1,700.00 -	1,305.00	756.45	03/2022 -	06/2022	3	-
235	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU	02/2015	760.00 -	1,536.00	1,233.08	03/2020 -	06/2022	27	-
236	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	1,720.00	701.37	03/2020 -	03/2025	60	-
237	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	2,910.84	1,621.40	02/2019 -	03/2025	73	-
238	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	1,567.00	-	03/2024 -	03/2026	24	-
239	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	2,172.16	262.36	03/2019 -	12/2027	105	-
	<u>West Central Railway</u>								
240	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH	06/2016	2,478.23 -	2,478.23	477.93	03/2022 -	03/2023	12	-
241	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH	08/2016	582.13 1,247.64	1,247.64	296.69	03/2022 -	03/2023	12	-
242	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH	12/2015	1,763.93 -	1,762.94	1,156.42	03/2020 -	03/2024	48	-
243	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	8,248.50	2,131.17	05/2008 -	03/2025	202	-
	Total		1,63,344.18 -	2,75,218.22	1,36,388.50				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>								
244	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]MoRTH,MADHYA PRADESH	11/2013	497.05 -	881.05	754.27	05/2017 -	04/2021	47	-
245	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]MoRTH,ANDHRA PRADESH	03/2016	995.09 995.00	995.09	476.77	05/2016 -	04/2021	59	-
246	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000958]MoRTH,RAJASTHAN	02/2018	370.30 -	370.30	290.00	06/2018 -	04/2021	34	-
247	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]MoRTH,WEST BENGAL	02/2018	218.70 218.70	218.70	104.09	11/2020 04/2020	04/2021	5	12
248	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH	11/2017	249.05 -	249.05	195.13	07/2018 03/2021	04/2021	33	1
249	BARASGAON TO RAHATEE - [N24001113]MoRTH,MAHARASHTRA	07/2016	289.11 290.00	289.11	101.90	09/2018 -	04/2021	31	-
250	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]MoRTH,UTTAR PRADESH	10/2013	445.89 653.00	653.29	754.40	03/2017 -	04/2021	49	-

Costing Rs. 150 Crore and above

(April 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
251	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]MoRTH,UTTAR PRADESH	03/2018	263.89 -	242.05	188.43	04/2020 -	04/2021	12	-
252	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAINCHAN - [N24000876]MoRTH,WEST BENGAL	01/2017	396.86 396.86	396.86	242.98	09/2019 11/2020	05/2021	20	6
253	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH,PUNJAB	03/2018	170.57 -	170.57	54.53	11/2020 -	05/2021	6	-
254	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969]MoRTH,ANDHRA PRADESH	01/2017	263.45 -	263.45	97.45	09/2017 -	05/2021	44	-
255	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA	02/2017	157.32 188.00	157.32	-	05/2019 -	05/2021	24	-
256	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]MoRTH,UTTAR PRADESH	03/2016	296.50 -	296.50	199.95	09/2020 -	05/2021	8	-
257	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]MoRTH,MIZORAM	08/2010	193.69 -	327.92	301.46	10/2010 -	06/2021	128	-
258	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH,MADHYA PRADESH	06/2015	390.51 -	390.51	257.01	- 03/2021	06/2021	-	3
259	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]MoRTH,MIZORAM	08/2010	195.04 -	377.99	331.49	10/2010 -	06/2021	128	-
260	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH	11/2015	628.45 -	628.45	439.63	01/2020 01/2021	06/2021	17	5
261	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH	03/2018	162.56 -	162.56	129.98	03/2018 -	06/2021	39	-
262	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH,MADHYA PRADESH	02/2018	169.63 -	169.63	46.52	03/2018 -	06/2021	39	-
263	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH	01/2017	205.05 -	205.05	123.20	03/2017 -	06/2021	51	-
264	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH	03/2018	233.04 -	233.04	158.22	03/2018 -	06/2021	39	-
265	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]MoRTH,MADHYA PRADESH	11/2017	254.17 -	254.17	164.68	02/2018 03/2021	06/2021	40	3
266	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH	02/2018	279.44 -	279.44	156.14	03/2018 12/2020	06/2021	39	6

Costing Rs. 150 Crore and above

(April 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
267	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000959]MoRTH,RAJASTHAN	02/2018	341.79 -	341.79	208.00	05/2018 -	06/2021	37	-
268	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]MoRTH,MIZORAM	08/2010	186.96 -	322.24	298.52	09/2014 -	06/2021	81	-
269	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 KM - [N24001230]MoRTH,UTTAR PRADESH	11/2018	281.45 -	281.45	72.05	12/2020 -	06/2021	6	-
270	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966]MoRTH,ANDHRA PRADESH	01/2016	348.95 -	348.95	200.57	08/2016 -	07/2021	59	-
271	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]MoRTH,TRIPURA	10/2016	171.90 -	171.90	123.81	08/2020 -	07/2021	11	-
272	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905]MoRTH,PUNJAB	03/2018	322.48 -	322.48	271.72	07/2020 -	08/2021	13	-
273	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH,PUNJAB	10/2017	1,069.59 -	1,069.59	692.14	10/2019 -	08/2021	22	-
274	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH	03/2018	214.69 -	214.69	69.34	03/2018 -	09/2021	42	-
275	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]MoRTH,MADHYA PRADESH	11/2011	954.43 -	1,191.51	235.61	09/2015 -	10/2021	73	-
276	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]MoRTH,WEST BENGAL	02/2018	426.18 426.18	426.18	249.01	09/2020 -	12/2021	15	-
277	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH,WEST BENGAL	06/2016	236.78 263.26	263.26	65.84	08/2019 -	12/2021	28	-
278	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGOUR SECTION BY EXECUTING BALANCE WORK FRO - [N24001241]MoRTH,RAJASTHAN	03/2020	255.23 -	255.23	1.66	08/2020 -	08/2022	24	-
279	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K - [N24001242]MoRTH,RAJASTHAN	08/2020	196.23 -	196.00	-	11/2020 -	08/2022	21	-
280	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH,WEST BENGAL	03/2016	160.27 213.97	213.97	25.64	08/2019 -	11/2022	39	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								

Costing Rs. 150 Crore and above

(April 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
281	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM	01/2016	294.17 -	294.17	121.82	01/2016 -	04/2021	63	-
282	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	387.00	245.80	08/2016 -	05/2021	57	-
283	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	339.55	252.49	08/2016 -	05/2021	57	-
284	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 -	340.00	193.99	08/2016 -	05/2021	57	-
285	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL,MANIPUR	08/2017	517.57 -	457.77	137.04	10/2018 -	10/2021	36	-
286	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND	03/2018	215.12 -	215.12	100.90	09/2018 -	11/2021	38	-
287	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM	06/2015	437.39 -	407.30	21.46	06/2018 -	12/2021	42	-
288	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM	06/2015	463.49 -	398.06	59.71	06/2018 -	12/2021	42	-
289	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND	03/2018	315.03 -	315.03	88.52	09/2018 -	12/2021	39	-
290	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND	03/2018	240.64 -	240.64	102.51	09/2018 -	12/2021	39	-
291	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND	03/2018	215.79 -	215.79	67.30	09/2018 -	12/2021	39	-
292	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH	01/2017	1,253.10 -	1,253.10	204.77	03/2017 -	03/2022	60	-
293	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND	03/2018	239.30 -	239.30	102.01	09/2018 -	05/2022	44	-
294	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND	03/2018	339.57 -	339.57	141.46	09/2018 -	07/2022	46	-

Costing Rs. 150 Crore and above

(April 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
295	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND	03/2018	285.68 -	285.68	77.91	09/2018 -	09/2022	48	-
296	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND	03/2018	272.89 -	272.89	51.17	09/2018 -	10/2022	49	-
297	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND	03/2018	500.09 336.49	336.49	79.51	09/2018 -	11/2022	50	-
298	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND	03/2018	323.98 -	323.98	42.54	09/2018 -	11/2022	50	-
299	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM	04/2017	519.09 -	519.09	56.58	09/2019 -	04/2023	43	-
300	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM	04/2017	473.18 -	473.18	81.00	09/2019 -	04/2023	43	-
301	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM	04/2017	537.82 -	537.82	100.74	09/2019 -	04/2023	43	-
302	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM	04/2017	642.96 -	642.96	82.00	09/2019 -	06/2023	45	-
303	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM	04/2017	518.53 -	518.53	108.99	09/2019 -	06/2023	45	-
304	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM	04/2017	640.07 -	640.07	3.25	09/2019 -	07/2023	46	-
305	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM	04/2017	428.11 -	428.11	48.03	09/2019 -	09/2023	48	-
306	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM	04/2017	404.29 -	404.29	17.77	09/2019 -	04/2024	55	-
National Highways Authority Of India									
307	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,295.18	08/2013 -	05/2021	93	-
308	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	227.77	36.08	03/2020 -	05/2021	14	-

Costing Rs. 150 Crore and above

(April 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
309	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	1,232.76	527.67	09/2017 -	05/2021	44	-
310	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	3,182.34	3,087.00	04/2015 01/2021	06/2021	74	5
311	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	504.00	385.08	05/2018 04/2019	06/2021	37	26
312	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	1,420.00	842.24	03/2020 -	06/2021	15	-
313	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	476.56	52.19	07/2017 -	06/2021	47	-
314	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN	04/2017	894.00 -	929.32	810.00	04/2020 -	07/2021	15	-
315	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	166.90	54.22	05/2013 -	08/2021	99	-
316	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21 -	289.21	194.57	- 02/2021	08/2021	-	6
317	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	2,128.72	1,070.00	04/2019 -	09/2021	29	-
318	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	2,485.93	827.64	06/2020 -	09/2021	15	-
319	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	546.00	307.08	07/2019 06/2021	12/2021	29	6
320	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	591.66	318.30	07/2019 06/2021	12/2021	29	6
321	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	870.00	333.68	03/2019 01/2021	12/2021	33	11
322	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 932.23	848.45	222.06	03/2020 -	12/2021	21	-
323	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	756.27	379.05	03/2020 -	12/2021	21	-
324	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE - [N24001231]NHAI,MADHYA PRADESH	02/2019	990.97 -	990.97	569.29	12/2019 -	12/2021	24	-
325	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHTH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	624.00	8.56	04/2014 -	01/2022	93	-
326	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	950.64	200.18	08/2017 -	02/2022	54	-
327	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53 -	291.53	150.06	- 08/2021	02/2022	-	6

Costing Rs. 150 Crore and above

(April 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
328	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	649.50	209.18	03/2019 12/2021	03/2022	36	3
329	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO - [N24001232]NHAI,MADHYA PRADESH	02/2019	847.00 -	847.00	393.93	03/2020 -	04/2022	25	-
330	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS-CONTROLLED EXPRESSWAY FROM BAWDI VILLAG - [N24001233]NHAI,MADHYA PRADESH	03/2019	1,047.00 -	1,047.00	367.12	05/2020 -	05/2022	24	-
331	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,878.70	08/2013 -	06/2022	106	-
332	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	1,176.37	462.14	08/2017 -	07/2022	59	-
333	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	1,227.87	566.14	09/2017 -	07/2022	58	-
334	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	3,379.45	2,901.20	03/2014 -	12/2022	105	-
	Total		52,137.14 -	54,574.68	30,119.95				
	<u>TELECOMMUNICATIONS</u>								
	<u>Bharat Sanchar Nigam Limited</u>								
335	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114]BSNL,MULTI STATE	03/2020	431.16 431.00	431.16	-	06/2021 -	11/2021	5	-
	<u>Central Public Works Department</u>								
336	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI	10/2016	248.20 -	248.20	145.26	03/2018 -	06/2021	39	-
	<u>Department Of Telecommunication</u>								
337	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	24,664.00	17,845.00	07/2015 -	07/2021	72	-
	Total		14,013.36 -	25,343.36	17,990.26				
	<u>URBAN DEVELOPMENT</u>								
	<u>Ahmedabad Metro Rail</u>								
338	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT	11/2014	10,773.00 -	12,787.00	8,768.08	12/2018 -	08/2022	44	-
	<u>Bangalore Metro Rail Corporation Limited</u>								
339	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA	02/2014	26,405.14 30,695.12	30,695.12	17,021.86	02/2019 03/2021	06/2024	64	39
	<u>Central Public Works Department</u>								
340	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI	06/2015	197.33 -	197.33	106.16	04/2019 06/2021	12/2021	32	6

Costing Rs. 150 Crore and above

(April 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
341	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 -	392.00	73.79	08/2020 -	03/2022	19	-
342	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I - [N28000128]CPWD,DELHI	10/2016	1,180.00 -	1,100.80	35.63	07/2021 -	12/2024	41	-
	<u>Delhi Metro Rail Corporation</u>								
343	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	38,585.00	39,182.53	03/2016 -	09/2021	66	-
344	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136]DMRC,DELHI	05/2017	565.00 -	565.00	438.37	12/2020 -	09/2021	9	-
	<u>Mumbai Metro Rail Corporation Ltd</u>								
345	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	33,406.00	17,039.36	01/2015 -	03/2023	98	-
	Total		1,01,233.47 -	1,17,728.25	82,665.78				
	<u>WATER RESOURCES</u>								
	<u>Brahmaputra Board</u>								
346	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPB,MAHARASHTRA	03/2017	233.57 -	233.57	173.71	12/2019 -	12/2021	24	-
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>								
347	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR - [N30000038]BUIDCO,BIHAR	04/2015	184.93 -	184.93	163.36	04/2020 -	06/2021	14	-
348	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]BUIDCO,BIHAR	03/2018	305.19 -	305.19	-	08/2021 -	12/2021	4	-
	<u>Delhi Jal Board</u>								
349	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI - [N30000017]DJB,DELHI	12/2018	515.07 -	515.07	336.27	01/2021 -	06/2021	5	-
350	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015]DJB,DELHI	05/2016	211.79 -	211.79	87.31	12/2021 -	12/2022	12	-
351	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]DJB,DELHI	05/2016	239.11 -	239.11	129.67	02/2022 -	12/2022	10	-
	<u>Kolkata Metropolitan Development Authority</u>								
352	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]KMDA, WEST BENGAL	05/2018	198.43 224.69	224.69	-	02/2022 -	06/2022	4	-
353	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH - [N30000042]KMDA, WEST BENGAL	05/2018	160.00 154.73	154.73	-	02/2022 -	10/2022	8	-
	<u>Polavaram Project Authority</u>								
354	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA,ANDHRA PRADESH	02/2009	10,151.04 55,548.87	55,548.87	17,325.20	03/2020 11/2021	04/2022	25	5
	<u>Uttar Pradesh Jal Nigam</u>								

Costing Rs. 150 Crore and above

(April 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
355	MATHURA SEWERAGE SCHEME - [N30000019]UPJalNigam,UTTAR PRADESH	12/2017	460.45 -	460.45	216.89	12/2020 -	05/2021	5	-
356	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]UPJalNigam,UTTAR PRADESH	03/2019	298.12 213.91	213.91	-	07/2021 -	06/2022	11	-
	Total		12,957.70 -	58,292.31	18,432.41				
	<u>DEFENCE PRODUCTION</u>								
	<u>Central Public Works Department</u>								
357	RESIDENTIAL QUATERS FOR HAL,BANGLORE - [N28000103]CPWD,KARNATAKA	12/2016	246.31 -	210.00	131.46	02/2020 -	12/2021	22	-
	Total		246.31 -	210.00	131.46				
	<u>HUMAN RESOURCE DEVELOPMENT</u>								
358	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]CPWD,PUNJAB	08/2016	294.00 -	350.69	276.69	04/2019 -	05/2021	25	-
359	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	111.29	03/2016 -	06/2021	63	-
360	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH	11/2017	171.72 -	171.72	53.94	03/2020 -	06/2021	15	-
361	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]CPWD,MAHARASHTRA	01/2018	223.37 -	223.37	61.35	07/2020 -	06/2021	11	-
362	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	498.99	224.58	06/2017 -	10/2021	52	-
363	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB - [N28000120]CPWD,PUNJAB	01/2018	430.00 -	387.83	199.99	05/2020 -	02/2022	21	-
364	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD,ODISHA	01/2019	790.79 -	790.79	173.98	03/2022 -	06/2022	3	-
365	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE,KANJIKODE WEST, DISTRICT PALAKKA - [N28000140]CPWD,KERALA	07/2019	753.63 -	753.63	58.47	03/2021 -	06/2022	15	-
366	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB. - [N28000142]CPWD,PUNJAB	10/2019	348.24 -	348.24	18.71	05/2022 -	08/2022	3	-
367	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A) - [N42000006]CPWD,KARNATAKA	07/2019	851.00 851.00	851.00	26.10	03/2022 -	09/2022	6	-
368	PERMANENT CAMPUS FOR IIM BODH GAYA - [N42000009]CPWD,BIHAR	09/2018	375.00 -	375.00	48.46	09/2020 -	11/2022	26	-

Costing Rs. 150 Crore and above

(April 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
369	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRICT - [N42000007]CPWD, ANDHRA PRADESH	09/2019	588.72 -	588.72	14.80	09/2022 -	01/2023	4	-
	Total		5,494.51 -	5,511.84	1,268.36				
	<u>HOME AFFAIRS</u>								
370	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD, DELHI	10/2013	1,219.21 -	2,000.00	906.04	10/2019 -	12/2021	26	-
	Total		1,219.21 -	2,000.00	906.04				
	<u>RURAL DEVELOPMENT</u>								
	<u>Hindustan Steelwork Construction Limited</u>								
371	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL, TRIPURA	03/2007	149.73 173.00	155.66	144.95	12/2015 -	10/2021	70	-
372	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL, TRIPURA	12/2007	202.61 227.00	207.12	190.22	12/2016 -	10/2021	58	-
373	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL, TRIPURA	10/2011	175.49 206.71	175.49	124.87	12/2016 -	12/2021	60	-
	Total		527.83 -	538.27	460.04				
	<u>DPIIT</u>								
	<u>Delhi Mumbai Industrial Corridor</u>								
374	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]DMIC, MULTI STATE	09/2011	12,579.09 -	13,812.30	8,915.05	09/2019 01/2014	07/2021	22	90
	<u>India International Convention And Expo Centre</u>								
375	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]IICC, DELHI	11/2017	4,773.00 -	5,178.00	2,557.37	12/2019 -	12/2021	24	-
	Total		17,352.09 -	18,990.30	11,472.42				
	Grand Total		6,04,676.92	8,28,116.80	4,59,908.57				

Details of Ongoing Projects having Time and Cost Overruns w.r.t Latest Schedule

Costing Rs. 150 Crore and above					(April 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
	<u>Bhavini Limited</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [N02000044]	09/2003	3,492.00 -	6,840.00	09/2010 -	10/2022	95.88	145
	<u>Nuclear Power Corporation Of India Limited</u>							
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	12/2015 -	02/2022	44.69	74
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]	10/2009	12,320.00 -	17,079.00	12/2016 -	03/2023	38.63	75
	Total		27,271.00 -	40,499.00				
	<u>CIVIL AVIATION</u>							
	<u>Airport Authority Of India Limited</u>							
4	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	07/2018	346.27 -	480.33	09/2021 -	09/2021	38.72	0
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]	12/2016	1,142.00 -	1,232.00	03/2021 -	03/2022	7.88	12
	Total		1,488.27 -	1,712.33				
	<u>COAL</u>							
	<u>Eastern Coal Fields Limited</u>							
6	RANIGANJ MASTER PLAN - [N06000163]	08/2009	2,661.73 -	5,146.48	08/2019 -	-	93.35	0
	<u>Neyveli Lignite Corporation</u>							
7	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80	11/2021 -	07/2022	.00	8
	<u>Singareni Colliers Company Limited</u>							
8	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	03/2015 -	03/2022	114.60	84
9	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	03/2019 -	03/2022	11.42	36
10	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 -	473.22	03/2015 -	03/2023	5.85	96
11	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86	132
	<u>Western Coal Fields Limited</u>							

Costing Rs. 150 Crore and above

(April 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
12	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]	09/2016	289.29 -	289.30	03/2022 -	03/2025	.00	36
13	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]	02/2016	198.68 -	325.18	03/2019 -	03/2022	63.67	36
14	ADASA UG TO OC - [N06000133]	08/2015	288.90 -	333.43	03/2023 -	03/2024	15.41	12
15	KOLAR PIMPRI EXTENSION OC - [N06000160]	03/2017	362.73 -	402.90	03/2020 -	09/2022	11.07	30
16	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	08/2016	319.76 -	404.45	03/2022 -	03/2022	26.49	0
17	BHANEGAON OC - [N06000121]	02/2015	187.94 -	409.68	03/2023 -	03/2023	117.98	0
18	NEW MAJRI UG TO OC - [N06000128]	05/2015	295.56 -	496.38	03/2019 -	09/2026	67.95	90
19	BHATADI EXPANSION OC MINE - [N06000150]	02/2016	304.52 -	729.86	03/2019 -	09/2026	139.68	90
	Total		23,571.99 -	27,530.00				
	<u>DPIIT</u>							
	<u>Delhi Mumbai Industrial Corridor</u>							
20	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]	09/2011	12,579.09 -	13,812.30	09/2019 -	07/2021	9.80	22
	<u>India International Convention And Expo Centre</u>							
21	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]	11/2017	4,773.00 -	5,178.00	12/2019 -	12/2021	8.49	24
	Total		17,352.09 -	18,990.30				
	<u>HEALTH AND FAMILY WELFARE</u>							
	<u>Central Public Works Department</u>							
22	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]	03/2019	1,577.00 -	1,828.00	09/2025 -	09/2025	15.92	0
	<u>Hospital Services Consultancy Corporation Ltd</u>							
23	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]	07/2016	152.95 -	177.92	02/2018 -	03/2021	16.33	37
24	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]	12/2017	156.56 -	190.34	- -	06/2021	21.58	0
25	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]	12/2014	168.90 -	191.20	05/2017 -	07/2019	13.20	26
26	CNCI KOLKATA WEST BENGAL - [N21000015]	08/2016	244.00 -	248.00	09/2018 -	05/2019	1.64	8
27	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]	01/2018	249.01 -	249.07	- -	01/2021	.02	0
28	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 -	250.00	05/2017 -	03/2021	22.29	46

Costing Rs. 150 Crore and above

(April 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
29	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017	08/2017	272.19 -	272.54	03/2019 -	03/2021	.13	24
30	AIIMS - OPD(NEW) - [N21000009	08/2014	293.65 -	325.00	05/2017 -	01/2020	10.68	32
31	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003	02/2013	414.11 -	499.23	11/2013 -	05/2021	20.55	90
32	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011	09/2014	505.58 -	585.00	03/2018 -	09/2019	15.71	18
	<u>National Building Construcion Corporation Ltd</u>							
33	AIIMS BILASPUR - [N21000028	04/2018	1,351.00 -	1,471.00	09/2021 -	09/2021	8.88	0
	Total		5,589.39 -	6,287.30				
	<u>HOME AFFAIRS</u>							
	<u>Central Public Works Department</u>							
34	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 -	2,000.00	10/2019 -	12/2021	64.04	26
	Total		1,219.21 -	2,000.00				
	<u>HUMAN RESOURCE DEVELOPMENT</u>							
35	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133	02/2019	186.00 199.00	205.00	09/2020 -	-	10.22	0
36	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102	08/2016	294.00 -	350.69	04/2019 -	05/2021	19.28	25
37	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100	02/2016	496.18 496.00	498.99	06/2017 -	10/2021	.57	52
38	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119	12/2016	549.31 -	559.47	07/2019 -	-	1.85	0
	<u>Rail India Technical And Economic Service</u>							
39	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001	09/2013	484.32 -	626.26	09/2014 -	-	29.31	0
	Total		2,009.81 -	2,240.41				
	<u>PETROLEUM</u>							
	<u>Hindustan Petroleum Corporation Limited</u>							
40	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296	09/2017	2,677.00 -	3,072.00	06/2021 -	08/2022	14.76	14

Costing Rs. 150 Crore and above

(April 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>Indian Oil Corporation Limited</u>							
41	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR), CACHAR, ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]	06/2016	423.00 -	502.00	08/2019 -	06/2021	18.68	22
	<u>Oil & Natural Gas Corporation Limited</u>							
42	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79 -	2,001.00	05/2013 -	02/2022	132.19	105
	<u>Oil India Limited</u>							
43	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	490.24	03/2017 -	-	39.05	48
44	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	01/2018	543.91 -	652.10	02/2020 -	06/2021	19.89	16
	Total		4,858.26 -	6,717.34				
	<u>POWER</u>							
	<u>National Thermal Power Corporation</u>							
45	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	07/2012	1,527.00 -	1,801.07	08/2017 -	-	17.95	0
46	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	10/2017 -	-	7.41	0
47	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	09/2014	9,188.98 -	9,842.02	07/2019 -	03/2021	7.11	20
48	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	03/2015	9,870.51 -	11,148.86	01/2020 -	-	12.95	0
49	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]	04/2012	9,750.89 -	12,176.28	02/2017 -	-	24.87	47
50	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	10/2017 -	-	7.55	0
51	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	15,105.22	01/2018 -	-	29.79	37
52	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,389.42	06/2019 -	10/2022	7.12	40
	<u>Power Grid Corporation Of India Limited</u>							
53	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03	07/2017 -	-	27.92	0
54	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	06/2014 -	-	31.17	0
55	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	03/2017	3,500.00 3,500.00	3,994.00	07/2020 -	06/2021	14.11	11
	<u>Satluj Jal Vidyut Nigam Limited</u>							
56	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	947.89	12/2021 -	12/2021	46.20	0

Costing Rs. 150 Crore and above

(April 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>Thdc India Limited</u>							
57	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,860.35	06/2013 -	12/2023	54.94	126
	Total		79,757.15 -	92,456.42				
	<u>RAILWAYS</u>							
	<u>Central Railways</u>							
58	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 -	315.00	03/2019 -	-	71.14	0
59	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	1,272.19 -	1,283.49	03/2022 -	03/2023	.89	12
60	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89 -	1,377.48	03/2021 -	03/2023	73.73	24
61	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	03/2023 -	03/2023	10.94	0
62	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 -	3,438.51	03/2024 -	03/2024	25.04	0
63	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	02/2015	3,627.47 3,627.00	3,627.47	03/2024 -	03/2023	.00	-12
64	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181]	02/1997	2,271.50 -	4,517.49	03/2021 -	03/2023	98.88	24
65	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 -	5,341.68	03/2024 -	03/2024	120.28	0
	<u>Container Corporation Of India</u>							
66	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 -	235.00	03/2019 -	-	.21	0
67	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]	01/2013	387.70 -	487.13	03/2018 -	-	25.65	36
	<u>East Central Railways</u>							
68	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	480.00	- -	-	125.34	0
69	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	499.41 -	516.02	03/2020 -	-	3.33	0
70	SAMASTIPUR-DARBANGHA - [N22000329]	05/2015	380.00 -	519.33	- -	03/2025	36.67	0
71	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	546.71	07/2014 -	-	64.60	0
72	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 -	549.75	- -	-	32.26	0
73	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	614.45	- -	12/2023	277.26	0
74	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]	04/1998	180.82 -	726.31	- -	-	301.68	0
75	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	325.00 -	735.20	- -	03/2021	126.22	0

Costing Rs. 150 Crore and above

(April 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
76	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	477.88 283.95	751.55	03/2012 -	07/2021	57.27	112
77	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181	04/2009	548.00 -	819.01	03/2020 -	03/2023	49.45	36
78	HAJIPUR - BACHAWARA - [N22000334	05/2015	678.54 -	929.86	03/2019 -	05/2021	37.04	26
79	MOTIHARI-SITAMARHI (NL) - [N22000174	04/2006	211.00 -	1,006.00	- -	-	376.78	0
80	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR [220100240	04/1997	324.73 -	1,070.00	03/2012 -	11/2022	229.50	128
81	MUZAFFARPUR SAGauli DOUBLING 100.60 KM - [N22000473	04/2016	731.64 -	1,185.73	03/2021 -	06/2022	62.06	15
82	SAGauli VALMIKINAGAR DOUBLING 109.7 KM - [N22000472	04/2016	744.04 -	1,215.54	03/2021 -	03/2024	63.37	36
83	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180	04/2004	372.14 -	1,470.50	- -	03/2023	295.15	0
84	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476	04/1991	329.39 -	1,483.14	- -	03/2022	350.27	0
85	KODERMA-TILAIYA (NL), ECR - [220100305	04/2002	459.91 -	1,625.87	- -	03/2023	253.52	0
86	CHHAPRA-MUZAFFARPUR (NL) - [N22000172	04/2006	378.56 -	1,858.75	- -	03/2023	391.01	0
87	HAJIPUR-SUGauli VIA VAISHALI (NL), ECR - [220100303	04/2003	528.65 -	2,066.78	- -	03/2023	290.95	0
88	BIHTA-AURANGABAD (NL) - [N22000170	04/2008	326.20 -	2,995.01	- -	03/2024	818.15	0
89	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222	03/1999	1,033.07 -	3,550.00	- -	03/2022	243.64	0
	<u>East Coast Railway</u>							
90	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380	04/2015	701.61 -	810.02	11/2018 -	03/2024	15.45	64
91	SAMBALPUR-TALCHER DOUBLING - [N22000315	03/2011	1,111.99 -	1,539.28	02/2019 -	12/2021	38.43	34
	<u>Eastern Railways</u>							
92	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218	04/2010	172.03 -	260.10	- -	03/2025	51.19	0
93	BAZAR SAU - AZIMGANJ JN. DOUBLING - [N22000302	04/2012	255.64 -	272.20	- -	03/2022	6.48	0
94	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241	04/2000	297.47 -	298.22	- -	03/2025	.25	0
95	MONIGRAM- NIMTITA - [N22000301	04/2012	250.93 -	310.70	- -	03/2024	23.82	0
96	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY [N22000239	04/2011	299.60 -	335.62	03/2017 -	03/2026	12.02	108

Costing Rs. 150 Crore and above

(April 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
97	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229	04/2010	365.17 -	439.30	03/2017 -	03/2025	20.30	96
98	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240	04/2010	494.54 -	494.59	03/2005 -	03/2025	.01	240
99	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238	04/2011	175.80 -	495.10	-	03/2022	181.63	0
100	BANDEL-BOINCHI 3RD LINE - [N22000221	04/2011	288.35 -	502.48	-	03/2021	74.26	0
101	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235	04/2010	365.17 -	527.54	-	03/2025	44.46	0
102	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216	04/1987	406.99 -	545.70	03/2006 -	03/2025	34.08	228
103	PIRPAINTI-BHAGALPUR - [N22000222	04/2011	261.38 -	565.00	-	05/2019	116.16	0
104	HANSDIHA-GODDA NL - [N22000236	04/2011	542.18 -	663.13	03/2020 -	03/2021	22.31	12
105	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHNACHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243	04/2009	499.96 -	680.68	02/2012 -	03/2025	36.15	157
106	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225	04/2005	595.51 -	769.40	03/2017 -	03/2025	29.20	96
107	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224	04/2001	923.52 -	995.10	03/2016 -	03/2025	7.75	108
108	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217	04/2007	450.00 -	1,261.34	-	03/2025	180.30	0
109	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	607.09 -	1,425.44	02/2013 -	03/2024	134.80	133
110	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	1,188.91 -	1,619.48	03/2019 12/2009	03/2025	36.22	72
111	PIRPAINTI-JASIDIH - [N22000219	04/2013	915.98 -	2,137.81	03/2022 -	03/2025	133.39	36
	<u>Indian Railway Construction Company Limited</u>							
112	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489	04/2013	3,055.00 -	3,055.15	09/2018 -	03/2022	.00	42
113	GEVRA ROAD PENDRA ROAD - [N22000488	02/2014	2,288.00 -	4,970.11	03/2022 -	12/2023	117.23	21
	<u>Metropolitan Rapid Transport Projects</u>							
114	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028	04/2006	495.74 -	734.01	06/2013 -	12/2021	48.06	102
115	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	2,980.41	03/2004 -	03/2022	501.57	216

Costing Rs. 150 Crore and above

(April 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
116	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [N220100268	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37	0
117	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135	03/2013	4,874.58 -	8,574.97	03/2016 -	06/2021	75.91	63
	<u>North Central Railway</u>							
118	ETAWAH-MAINPURI (NL),NCR - [N220100318	04/1997	120.00 -	346.00	12/2008 -	-	188.33	0
119	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372	04/2015	668.70 668.00	680.00	03/2020 -	-	1.69	0
120	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	04/2011	2,912.96 -	3,845.60	03/2022 -	12/2024	32.02	33
	<u>North East Frontier Railway</u>							
121	KISHANGANJ JALALGARH, NL, NEFR - [N22000101	04/2008	333.76 -	360.00	- -	-	7.86	0
122	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207	04/2010	241.52 -	373.87	- -	12/2021	54.80	0
123	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193	04/2010	221.42 -	380.00	- -	-	71.62	0
124	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206	04/2010	242.22 -	471.00	03/2020 -	-	94.45	0
125	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [N220100135	04/1983	297.32 -	614.00	03/2019 -	-	106.51	0
126	AGARTALA-AKHAURA NL - [N22000195	04/2012	569.63 -	742.00	03/2020 -	03/2022	30.26	24
127	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210	04/2011	314.00 -	800.00	03/2019 -	03/2021	154.78	24
128	MURKONGSELEK-PASIGHAT NL - [N22000208	04/2011	414.84 -	1,040.00	03/2020 -	-	150.70	0
129	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086	09/2006	385.20 -	1,043.00	03/2019 -	03/2023	170.77	48
130	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499	02/1999	380.60 -	1,090.60	04/2010 -	-	186.55	0
131	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHAWA JAINTI - [N22000209	04/1999	819.23 -	1,871.00	- -	-	128.39	0
132	DIGARU-HOJAI (102 KM) - [N22000389	04/2015	870.96 -	1,873.21	03/2021 -	05/2021	115.07	2
133	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390	04/2016	602.27 -	2,144.78	12/2021 -	04/2021	256.12	-8
134	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087	09/2006	532.87 -	2,145.00	03/2019 -	03/2024	302.54	60
135	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388	04/2015	2,232.32 -	2,950.00	03/2022 -	03/2023	32.15	12

Costing Rs. 150 Crore and above

(April 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
136	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205	04/2010	906.46 -	4,083.02	03/2021 -	-	350.44	0
137	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	1,180.19 -	4,541.38	12/2008 -	05/2021	284.80	149
138	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	2,393.47 -	5,521.45	03/2014 -	03/2023	130.69	108
139	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124	04/2006	2,326.52 -	6,911.00	03/2015 -	12/2024	197.05	117
140	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	8,600.00	12/2015 -	-	542.04	0
141	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	4,454.17 -	12,264.15	03/2011 -	12/2023	175.34	153
	<u>North Eastern Railway</u>							
142	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321	04/2014	182.92 -	197.73	- -	-	8.10	0
143	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456	04/2016	213.00 -	213.35	04/2016 -	12/2021	.16	68
144	KICHHA-KHATIMA (NL) - NER - [220100317	04/2003	142.45 -	228.40	- -	-	60.34	0
145	CHHAPRA-BALLIA UP - [N22000134	03/2013	295.00 -	477.31	01/2019 -	02/2022	61.80	37
146	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136	03/2013	643.00 -	644.00	- -	-	.16	0
147	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468	04/2016	602.50 -	714.34	- -	12/2023	18.56	0
148	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131	03/2007	243.78 -	895.00	12/2021 -	12/2021	267.13	0
149	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130	03/2013	307.00 -	1,409.09	- -	-	358.99	0
150	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460	04/2017	1,343.00 -	1,476.15	01/2018 -	-	9.91	0
	<u>North Western Railway</u>							
151	THIYAT HAMIRA-SANU - [N22000149	04/2013	236.93 -	350.45	10/2018 -	01/2020	47.91	15
152	AJMER-BANGURGRAM - [N22000155	04/2011	213.39 -	375.00	11/2019 -	03/2021	75.73	16
153	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137	04/2012	246.08 -	395.00	12/2019 -	02/2021	60.52	14
154	PUSHKAR-MERTA - [N22000151	04/2013	323.00 -	432.22	- -	-	33.81	0
155	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152	04/2013	420.18 -	480.00	03/2020 -	06/2021	14.24	15
156	ALWAR-BANDIKUI DOUBLING - [N22000157	04/2013	242.09 -	525.00	02/2019 -	02/2020	116.86	12

Costing Rs. 150 Crore and above

(April 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
157	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	701.81	03/2020 -	10/2022	16.97	31
158	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	860.41	02/2019 -	06/2022	109.82	40
159	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]	04/2013	822.00 -	1,099.00	- -	-	33.70	0
160	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]	05/2015	873.71 -	1,980.21	- -	-	126.64	0
161	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	4,262.36	- -	-	104.65	0
	<u>Northern Railway</u>							
162	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63	- -	-	57.68	0
163	GRADE SEPARATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	359.00	- -	03/2024	129.17	0
164	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]	04/2012	295.68 -	419.00	- -	09/2023	41.71	0
165	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]	04/2007	336.91 -	791.39	- -	03/2023	134.90	0
166	QADIAN-BEAS - [N22000295]	04/2011	205.22 -	841.90	- -	03/2024	310.24	0
167	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 -	859.00	03/2016 -	06/2021	37.44	63
168	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	893.45	12/2011 -	06/2021	211.31	114
169	UNCHAHAAR-AMETHI - [N22000294]	04/2012	1,229.00 -	1,265.00	- -	03/2023	2.93	0
170	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,200.00	07/2012 -	03/2024	388.89	140
171	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	27,949.00	11/2002 -	12/2022	1,017.96	241
	<u>Rail Vikas Nigam Ltd.</u>							
172	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	396.00	03/2009 03/2009	-	196.83	0
173	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	04/2015	773.94 -	850.00	12/2024 -	12/2024	9.83	0
174	DHASA-JETALSAR (GC) - [N22000141]	04/2012	644.38 -	872.65	03/2021 -	03/2021	35.42	0
175	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	950.00	03/2016 -	12/2021	50.15	69
176	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	943.60 -	1,000.00	03/2022 -	12/2024	5.98	33
177	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,400.00	03/2019 -	06/2022	51.02	39
178	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	975.62 -	1,500.00	12/2021 -	12/2021	53.75	0
179	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 -	1,536.00	03/2019 -	06/2022	62.89	39

Costing Rs. 150 Crore and above

(April 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
180	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	03/2012	1,183.25 -	1,825.00	12/2020 -	12/2022	54.24	24
181	BINA - KOTA DOUBLING WITH RE - [N22000414]	04/2011	1,485.85 -	1,835.83	12/2020 -	12/2021	23.55	12
182	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	1,185.64 -	1,844.47	12/2017 -	-	55.57	0
183	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	04/2013	1,548.66 -	1,868.89	12/2021 -	03/2022	20.68	3
184	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 -	2,009.00	03/2020 -	12/2021	111.91	21
185	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	1,202.70 -	2,440.53	02/2015 -	06/2022	102.92	88
186	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 -	2,725.00	03/2020 -	12/2021	281.93	21
187	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95	141
188	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 -	3,000.00	03/2023 -	12/2022	41.04	-3
189	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 -	3,327.72	12/2024 -	12/2026	42.47	24
190	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]	03/2012	1,503.71 -	3,377.00	03/2020 -	03/2022	124.58	24
191	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.68	12/2023 -	12/2023	9.32	0
192	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2025	7.78	108
193	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	04/2010	2,913.51 -	4,639.00	03/2016 -	03/2025	59.22	108
194	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	2,966.99 -	6,753.42	12/2026 -	12/2025	127.62	-12
195	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	04/2011	16,216.00 -	22,716.11	12/2024 -	03/2025	40.08	3
	<u>Railway Electrification</u>							
196	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	-	60.77	0
	<u>South Central Railway</u>							
197	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	04/2017	119.73 185.00	449.39	03/2022 -	12/2022	275.34	9
198	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	704.31 -	927.94	03/2020 -	06/2021	31.75	15
199	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]	03/1996	164.36 -	1,050.00	02/2009 -	-	538.84	0

Costing Rs. 150 Crore and above

(April 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
200	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	04/2012	1,856.95 -	1,952.68	03/2023 -	03/2024	5.16	12
201	KOTLPALLI-NARASAPUR (NL) (SCR) - [N220100265]	12/2001	1,045.20 -	2,120.16	03/2009 -	03/2024	102.85	180
202	NADIKUDE-SRI KALAHASTI - [N22000286]	04/2011	2,288.70 -	2,643.25	03/2021 -	03/2024	15.49	36
203	MANUGURU-RAMAGUNDAM - [N22000259]	04/2013	1,112.00 -	2,911.84	- -	-	161.86	0
204	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]	04/2008	2,132.77 -	3,037.95	03/2014 -	03/2027	42.44	156
205	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	1,723.00 1.00	3,421.35	03/2000 -	03/2023	98.57	276
206	GUNTUR-GUNTAKAL - [N22000368]	04/2016	3,631.00 -	3,887.48	03/2022 -	03/2024	7.06	24
	<u>South East Central Railway</u>							
207	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00 -	1,096.00	12/2021 -	12/2024	378.60	36
208	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]	04/2008	872.00 -	1,226.51	12/2019 -	-	40.65	0
209	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438]	04/2010	585.93 -	1,268.32	02/2019 -	12/2021	116.46	34
210	ANUPPUR-KATNI - [N22000485]	04/2015	1,370.00 -	1,370.94	12/2021 -	12/2023	.07	24
211	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	1,413.76	- -	-	268.37	0
212	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	511.86 -	2,005.25	04/2020 -	-	291.76	12
213	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	04/2015	1,973.00 -	2,135.34	03/2021 -	12/2023	8.23	33
214	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,908.51 -	3,524.81	03/2023 -	12/2023	84.69	9
	<u>South Eastern Railway</u>							
215	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION [N22000162]	04/2010	149.90 -	230.00	03/2015 -	-	53.44	0
216	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND [N22000323]	04/2012	148.77 -	377.00	12/2016 -	08/2020	153.41	44
217	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	620.00	- -	03/2025	131.89	0
218	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	651.00 -	1,009.00	03/2015 -	03/2025	54.99	120
219	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	-	160.76	0
220	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL [N22000402]	04/1998	1,027.40 -	2,373.00	03/2003 -	03/2030	130.97	324
	<u>South Western Railway</u>							

Costing Rs. 150 Crore and above					(April 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
221	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	12/2023	14.14	0
222	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	296.10	- -	12/2023	.03	0
223	ARSIKERE-TUMKUR - [N22000332]	03/2015	578.00 -	783.00	03/2020 -	06/2021	35.47	15
224	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78 -	998.00	03/2017 -	03/2025	54.78	96
225	YELAHANKA-PENUKONDA - [N22000328]	05/2015	860.43 -	1,147.00	03/2020 -	06/2021	33.31	15
226	HUBLI- CHIKJAJUR - [N22000325]	03/2015	1,156.94 -	1,656.00	03/2020 -	03/2023	43.14	36
227	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 -	1,870.41	03/2019 -	03/2024	15.84	60
228	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	1,801.01 -	1,967.00	- -	12/2023	9.22	0
229	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	2,062.30 -	2,432.50	- -	03/2025	17.95	0
230	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	2,315.00 -	3,911.65	- -	12/2024	68.97	0
	<u>Southern Railway</u>							
231	ERNAKULAM-KUMBALAM - [N22000204]	04/2010	189.24 -	275.21	- -	-	45.43	0
232	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]	10/2013	187.26 -	327.00	04/2014 -	-	74.62	80
233	KUMBALAM-TURAVUR - [N22000191]	04/2011	252.96 -	369.55	- -	-	46.09	0
234	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	457.08	- -	12/2021	69.20	0
235	ATTIPPATTU PUTTUR - [N22000184]	04/2008	151.84 -	527.37	02/2019 -	-	247.32	0
236	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	559.95	- -	03/2024	181.84	0
237	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	608.13	- -	09/2021	269.89	0
238	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	02/1996	268.87 -	950.00	03/2005 -	09/2021	253.33	198
239	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	931.98 -	1,121.00	- -	05/2021	20.28	0
240	ERODE-PALANI - [N22000199]	04/2008	288.57 -	1,140.00	- -	-	295.05	0
241	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,205.00	- -	03/2024	130.17	0
242	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]	02/2015	1,000.00 -	1,246.00	- -	-	24.60	0

Costing Rs. 150 Crore and above

(April 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
243	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186	04/2013	839.00 -	1,500.00	- -	-	78.78	0
244	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451	02/2015	760.00 -	1,536.00	03/2020 -	06/2022	102.11	27
245	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	303.98 -	1,720.00	03/2020 -	03/2025	465.83	60
246	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215	04/2011	120.70 -	2,172.16	03/2019 -	12/2027	1,699.64	105
247	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	1,566.00 -	2,815.62	- -	-	79.80	0
248	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' - AGASTIYAMPALLI - [N22000079	09/2007	724.69 -	2,910.84	02/2019 -	03/2025	301.67	73
<u>West Central Railway</u>								
249	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314	04/2001	424.60 -	2,909.99	03/2021 -	03/2023	585.35	24
250	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	247.66 -	8,248.50	05/2008 -	03/2025	3,230.57	202
<u>Western Railway</u>								
251	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125	04/2006	117.36 196.95	202.35	03/2011 -	-	72.42	0
Total			1,88,639.64 -	3,76,212.69				
<u>ROAD TRANSPORT AND HIGHWAYS</u>								
<u>Ministry Of Road Transport And Highways (State Pwds)</u>								
252	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646	06/2016	157.30 157.00	157.30	06/2018 -	-	.00	0
253	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872	03/2018	166.21 -	173.41	08/2018 -	-	4.33	0
254	JALGAON TO NANDURA - [N24001088	03/2018	177.84 177.00	177.84	12/2019 -	-	.00	0
255	CHIKALI TO DHAD - [N24001061	03/2018	189.46 189.00	189.46	12/2019 -	-	.00	0
256	WADIGODRI TO DHANGRIIMPRI - [N24001063	03/2018	194.23 194.00	194.23	02/2020 -	-	.00	0
257	KHAMGAON TO SHEGAON - [N24001009	02/2017	203.21 203.00	203.21	05/2019 -	-	.00	0
258	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140	11/2016	215.16 215.00	215.16	09/2019 -	-	.00	0
259	DHANGIIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064	03/2018	217.14 217.00	217.14	02/2020 -	-	.00	0

Costing Rs. 150 Crore and above

(April 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
260	MANGRUPHIR TO MAHAN - [N24001087	03/2018	222.13 222.00	222.13	11/2019 -	-	.00	0
261	KUNDRAL TO WAZAR - [N24001077	01/2018	225.25 225.00	225.25	12/2019 -	-	.00	0
262	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890	03/2018	217.22 -	226.88	08/2018 -	09/2021	4.45	37
263	PALPHATA TO PHULAMBARI - [N24001060	03/2018	227.19 227.00	227.19	12/2019 -	-	.00	0
264	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820	11/2017	237.80 -	238.00	11/2019 -	-	.08	0
265	PARBHANI TO GANGKHED - [N24001065	03/2018	238.19 238.00	238.19	12/2019 -	-	.00	0
266	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141	03/2016	240.30 240.00	240.30	01/2020 -	03/2021	.00	14
267	NAIGAONBANDI TO MANGRULPIR - [N24001094	12/2017	244.04 244.00	244.04	03/2019 -	-	.00	0
268	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276	12/2011	156.26 227.00	247.95	- -	-	58.68	0
269	SANGOLA TO JATH - [N24001052	01/2018	257.38 257.00	257.38	12/2019 -	-	.00	0
270	TALEGAON TO GONAPUR - [N24001096	01/2018	264.41 264.00	264.41	03/2019 -	-	.00	0
271	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316	03/2015	258.97 -	268.92	08/2015 -	-	3.84	0
272	OMREGA TO AUSA - [N24001067	03/2018	272.04 272.00	272.04	12/2019 -	-	.00	0
273	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259	03/2015	280.16 -	290.59	- -	-	3.72	0
274	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938	03/2018	297.12 294.00	294.12	07/2018 -	-	-1.01	0
275	BHOKAR TO SARSAM - [N24001128	02/2017	295.09 -	295.99	07/2019 -	-	.31	0
276	KOTHARI TO DHANORA - [N24001073	09/2018	301.38 301.00	301.38	08/2020 -	-	.00	0
277	MALEGAON TO RISOD - [N24001089	02/2018	303.24 303.00	303.24	12/2019 -	-	.00	0
278	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398	01/1991	282.41 -	322.01	08/2016 -	-	14.02	0
279	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181	08/2010	186.96 -	322.24	09/2014 -	06/2021	72.36	81
280	MEHKAR TO CHIKALI - [N24001011	02/2017	322.48 322.00	322.48	05/2019 -	-	.00	0

Costing Rs. 150 Crore and above

(April 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
281	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308	08/2010	193.69 -	327.92	10/2010 -	06/2021	69.30	128
282	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062	03/2018	336.21 336.00	336.21	12/2019 -	-	.00	0
283	LATUR TO PANGAON - [N24001066	03/2018	336.47 336.00	336.47	12/2019 -	-	.00	0
284	MORSHI TO ACHALPUR - [N24001015	01/2017	341.16 341.00	341.16	06/2019 -	-	.00	0
285	OSMANNAGAR TO KUNDRAL - [N24001075	09/2017	344.25 344.00	344.25	08/2020 -	-	.00	0
286	KARAD TO VITA - [N24001049	01/2018	344.85 245.00	344.85	12/2019 -	-	.00	0
287	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	09/2017 -	-	36.24	0
288	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407	10/2015	333.21 -	353.89	11/2015 -	-	6.21	0
289	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928	10/2015	333.21 -	355.89	12/2015 -	-	6.81	0
290	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531	01/1991	319.68 -	369.77	- -	-	15.67	0
291	SHEGAON TO DEORI PHATA - [N24001010	02/2017	373.10 373.00	373.10	05/2019 -	-	.00	0
292	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402	01/1991	358.22 -	377.64	10/2016 -	-	5.42	0
293	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415	08/2010	195.04 -	377.99	10/2010 -	06/2021	93.80	128
294	PANCHARAL TO MANDANGHAR - [N24001107	07/2018	381.08 302.00	381.08	05/2020 -	-	.00	0
295	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311	03/2012	207.03 -	389.45	05/2012 -	-	88.11	0
296	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392	11/2010	268.08 -	390.73	05/2017 -	-	45.75	0
297	DIGRAS DARWAH KARANJA - [N24001013	01/2017	391.06 391.00	391.06	06/2019 -	-	.00	0
298	CHIKLI TO TAKARKHED - [N24001083	03/2018	393.10 393.00	393.10	12/2019 -	-	.00	0
299	SELDOH TO PANVAR - [N24001097	07/2018	404.33 404.00	404.33	05/2020 -	-	.00	0
300	KARAD PATAN CHIPLUN GUHAGAR - [N24001057	02/2017	407.19 407.00	407.19	06/2019 -	-	.00	0
301	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056	02/2017	422.02 422.00	422.02	07/2019 -	-	.00	0

Costing Rs. 150 Crore and above

(April 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
302	ARDHAPUR TO HIMAYATNAGAR - [N24001079]	12/2017	426.06 426.00	426.06	06/2020 -	-	.00	0
303	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]	03/2018	460.73 -	461.00	- -	-	.06	0
304	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]	03/2018	504.19 504.00	504.19	11/2018 -	-	.00	26
305	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]	03/2016	536.65 356.00	536.65	12/2019 -	06/2021	.00	18
306	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]	01/2016	476.20 544.00	544.00	09/2016 -	06/2021	14.24	57
307	CHIKALI TO KHAMGAON - [N24001012]	02/2017	548.03 548.00	548.03	06/2019 -	-	.00	0
308	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAF LONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]	11/2010	470.20 -	630.36	02/2011 -	-	34.06	0
309	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]	10/2013	445.89 -	653.29	03/2017 -	-	46.51	0
310	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]	10/2013	445.89 653.00	653.29	03/2017 -	04/2021	46.51	49
311	BHOGAN KHURD TO KASHEDI - [N24001132]	09/2017	743.21 743.00	743.21	06/2021 -	06/2021	.00	0
312	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]	11/2013	497.05 -	881.05	05/2017 -	-	77.26	47
313	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]	11/2015	889.24 -	904.82	- -	-	1.75	0
314	PARSHURAM GHAT TO ARAWALI - [N24001133]	04/2016	983.14 983.00	983.14	12/2019 -	-	.00	0
315	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]	11/2010	624.41 -	992.67	03/2011 -	-	58.98	117
316	REHABILITATION AND UPGRADATION OF KARNATAKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]	03/2016	995.09 995.00	995.09	05/2016 -	-	.00	59
317	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]	11/2011	954.43 -	1,191.51	09/2015 -	10/2021	24.84	73
318	KANTE TO WAKED - [N24001134]	03/2016	1,230.02 1,230.00	1,230.02	11/2019 -	-	.00	0
319	KALMATH TO ZARAP - [N24001137]	09/2016	1,338.13 1,338.00	1,338.13	03/2020 -	-	.00	0
320	VADPALE TO BHOGAN KHURD - [N24001115]	01/2017	1,598.47 1,560.00	1,598.47	11/2019 -	-	.00	0
321	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]	09/2011	1,979.00 -	2,036.90	- -	-	2.93	0

Costing Rs. 150 Crore and above					(April 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>							
322	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681	01/2017	194.66 -	252.05	04/2017 -	-	29.48	0
323	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690	01/2017	198.22 -	252.05	04/2017 -	-	27.16	0
324	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679	02/2017	195.23 -	252.79	04/2017 -	-	29.48	0
325	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680	02/2017	203.36 -	263.31	04/2017 -	-	29.48	0
326	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686	03/2016	373.07 -	387.00	08/2016 -	05/2021	3.73	57
327	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695	04/2017	388.00 -	447.37	10/2017 -	-	15.30	0
328	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902	10/2017	818.00 -	887.68	- -	-	8.52	0
	<u>National Highways Authority Of India</u>							
329	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049	12/2003	160.00 -	167.98	05/2008 -	06/2019	4.99	133
330	NALBARI T BIJNI (AS-7) - [N24000048	12/2003	208.00 -	230.00	04/2008 -	02/2021	10.58	154
331	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	255.23	11/2008 -	-	64.62	0
332	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725	01/2018	273.46 -	276.17	- -	-	.99	0
333	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631	11/2016	290.73 -	315.00	- -	-	8.35	0
334	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607	08/2016	323.72 -	336.60	08/2018 -	-	3.98	0
335	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	340.14	04/2009 -	-	70.23	0
336	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063	12/2003	217.61 -	360.84	04/2010 -	07/2019	65.82	111
337	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437	10/2015	361.15 -	363.93	- -	-	.77	0
338	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572	05/2016	364.56 -	392.00	- -	04/2021	7.53	0
339	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279	12/2003	167.64 -	435.78	11/2008 -	-	159.95	0
340	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713	12/2017	404.94 -	448.18	- -	10/2020	10.68	0

Costing Rs. 150 Crore and above					(April 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
341	INDORE-DEWAS(NH-3) - [N24000159]	11/2010	325.00 -	475.00	05/2013 -	-	46.15	0
342	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- [N24000594]	07/2016	458.03 -	486.00	- -	-	6.11	0
343	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	520.00	02/2009 -	-	85.71	0
344	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]	03/2018	496.20 -	537.17	- -	-	8.26	0
345	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]	05/2011	511.54 -	591.00	11/2013 -	01/2021	15.53	86
346	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]	08/2015	516.13 -	649.27	04/2018 -	-	25.80	0
347	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	655.17	07/2009 -	-	234.27	0
348	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]	01/1991	642.41 -	681.67	- -	-	6.11	0
349	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]	10/2015	593.26 -	690.17	05/2018 -	06/2021	16.34	37
350	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]	03/2015	794.30 -	691.38	- -	05/2020	-12.96	0
351	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]	11/2012	605.84 -	722.46	07/2018 -	-	19.25	0
352	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]	10/2015	531.13 -	730.97	05/2018 -	06/2021	37.63	37
353	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	03/2017	672.89 -	736.01	03/2020 -	-	9.38	0
354	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]	10/2019	743.88 -	743.89	- -	12/2021	.00	0
355	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]	10/2015	447.29 -	746.43	12/2017 -	-	66.88	0
356	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	03/2017	754.54 -	756.27	03/2020 -	12/2021	.23	21
357	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]	03/2018	795.50 -	799.30	- -	07/2021	.48	0
358	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]	03/2018	642.13 -	807.00	- -	-	25.68	0
359	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]	08/2015	814.04 -	825.17	- -	10/2021	1.37	0

Costing Rs. 150 Crore and above

(April 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
360	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]	12/2017	656.98 -	840.00	- -	11/2022	27.86	0
361	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214]	12/2017	217.96 -	884.00	- -	-	305.58	0
362	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]	04/2017	894.00 -	929.32	04/2020 -	07/2021	3.95	15
363	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]	03/2018	634.70 -	931.21	- -	07/2021	46.72	0
364	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]	06/2015	845.24 -	941.00	- -	-	11.33	0
365	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	03/2017	744.64 -	982.00	03/2020 -	-	31.88	0
366	MEERUT-BULANDSHAHR - [N24000539]	01/2016	683.24 -	987.94	- -	-	44.60	0
367	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]	08/2015	854.80 -	1,038.56	- -	-	21.50	0
368	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	03/2017	988.34 -	1,043.28	03/2020 -	-	5.56	0
369	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	03/2017	1,030.44 -	1,065.51	03/2020 -	-	3.40	0
370	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]	03/2017	1,059.73 -	1,071.00	03/2017 -	-	1.06	0
371	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]	03/2018	1,016.92 -	1,071.00	- -	01/2022	5.32	0
372	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]	09/2016	950.69 -	1,108.00	08/2019 -	-	16.55	0
373	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]	02/2016	997.15 -	1,115.95	03/2019 -	-	11.91	0
374	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]	09/2016	1,100.19 -	1,145.31	- -	03/2021	4.10	0
375	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]	03/2017	1,098.06 -	1,160.64	03/2020 -	-	5.70	0
376	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]	03/2017	831.58 -	1,177.00	03/2020 -	-	41.54	0
377	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]	12/2015	1,167.45 -	1,182.94	- -	-	1.33	0

Costing Rs. 150 Crore and above					(April 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
378	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 -	1,187.10	03/2020 -	-	13.97	0
379	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793	03/2018	925.40 -	1,197.00	- -	-	29.35	0
380	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704	09/2017	1,124.11 -	1,232.76	09/2017 -	05/2021	9.67	44
381	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814	03/2018	1,029.96 -	1,261.05	- -	03/2021	22.44	0
382	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831	03/2018	1,294.47 -	1,296.00	- -	-	.12	0
383	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785	02/2018	1,166.26 -	1,296.93	- -	08/2021	11.20	0
384	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.71 -	1,310.00	03/2020 -	-	10.58	0
385	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800	03/2018	1,120.57 -	1,332.00	- -	-	18.87	0
386	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 -	1,420.00	03/2020 -	06/2021	10.24	15
387	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	03/2020 -	-	44.39	0
388	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801	02/2018	1,052.21 -	1,449.00	- -	01/2021	37.71	0
389	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233	04/2014	1,266.60 -	1,544.00	09/2016 -	-	21.90	0
390	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494	05/2013	1,055.00 -	1,601.77	11/2015 -	-	51.83	0
391	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621	09/2016	1,239.82 -	1,727.66	- -	-	39.35	0
392	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463	12/2015	1,083.00 -	1,827.15	06/2018 -	-	68.71	0
393	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784	02/2018	1,424.77 -	1,853.42	- -	-	30.09	0
394	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790	03/2018	1,261.98 -	1,952.20	- -	07/2021	54.69	0
395	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693	06/2017	1,958.88 -	1,993.81	06/2020 -	02/2021	1.78	8

Costing Rs. 150 Crore and above

(April 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
396	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830	03/2018	2,065.96 -	2,169.00	- -	-	4.99	0
397	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601	08/2016	1,169.61 -	2,280.00	- -	-	94.94	0
398	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515	04/2014	1,665.00 -	2,360.65	- -	-	41.78	0
399	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787	02/2018	1,995.34 -	2,400.00	- -	11/2021	20.28	0
400	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 -	2,447.00	03/2020 -	-	18.50	0
401	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789	02/2018	2,177.80 -	2,450.00	- -	-	12.50	0
402	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807	03/2018	1,532.62 -	2,499.00	03/2021 -	04/2021	63.05	1
403	NASHRI- CHANANI - [N24000162	05/2011	2,159.00 -	2,519.00	06/2015 -	-	16.67	0
404	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600	08/2016	1,388.34 -	2,587.50	09/2019 -	-	86.37	0
405	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,967.50	11/2011 -	-	167.82	0
406	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551	03/2016	1,587.49 -	2,982.00	04/2019 -	-	87.84	0
407	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224	10/2012	1,928.22 -	3,182.34	04/2015 -	06/2021	65.04	74
408	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182	09/2011	2,848.00 -	3,379.45	03/2014 -	12/2022	18.66	105
	Total		1,07,225.71 -	1,32,093.27				
	<u>TELECOMMUNICATIONS</u>							
	<u>Bharat Sanchar Nigam Limited</u>							
409	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114	03/2020	431.16 431.00	431.16	06/2021 -	11/2021	.00	5
	<u>Department Of Telecommunication</u>							
410	NETWORK FOR SPECTRUM - [N26000101	03/2012	13,334.00 -	24,664.00	07/2015 -	07/2021	84.97	72
	Total		13,765.16 -	25,095.16				
	<u>URBAN DEVELOPMENT</u>							
	<u>Ahmedabad Metro Rail</u>							

Costing Rs. 150 Crore and above

(April 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
411	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]	11/2014	10,773.00 -	12,787.00	12/2018 -	08/2022	18.69	44
	<u>Chennai Metro Rail Ltd</u>							
412	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]	02/2009	14,600.00 -	19,058.00	12/2015 -	-	30.53	0
	<u>Kochi Metro Rail Corporation Ltd</u>							
413	KOCHI METRO RAIL PROJECT - [N28000081]	07/2012	5,181.79 -	6,218.14	07/2017 -	-	20.00	38
	<u>Mumbai Metro Rail Corporation Ltd</u>							
414	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]	07/2013	23,136.00 -	33,406.00	01/2015 -	03/2023	44.39	98
	<u>National Building Construcion Corporation Ltd</u>							
415	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	06/2012	4,264.00 -	4,720.73	11/2019 -	-	10.71	0
	Total		57,954.79 -	76,189.87				
	<u>WATER RESOURCES</u>							
	<u>Uttar Pradesh Jal Nigam</u>							
416	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]	01/2019	231.79 -	234.03	12/2021 -	12/2021	.97	0
417	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]	02/2019	681.78 -	690.71	06/2022 -	06/2022	1.31	0
	Total		913.57 -	924.74				
	Grand Total		5,31,616.04	8,08,948.83				

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Annexure - XIII

Costing Rs. 150 Crore and above					(April 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 - 5,677.00	6,840.00	09/2010 -	10/2022	95.88
	<u>Nuclear Power Corporation Of India Limited</u>						
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 - 11,459.00	16,580.00	12/2015 -	02/2022	44.69
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]	10/2009	12,320.00 - 12,320.00	17,079.00	12/2016 -	03/2023	38.63
	Total		27,271.00 .00 29,456.00	40,499.00			
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
4	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	07/2018	346.27 - 346.27	480.33	09/2021 -	09/2021	38.72
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI [N04000083]	12/2016	1,142.00 - 1,142.00	1,232.00	03/2021 -	03/2022	7.88
	Total		1,488.27 .00 1,488.27	1,712.33			
	<u>COAL</u>						
	<u>Eastern Coal Fields Limited</u>						
6	RANIGANJ MASTER PLAN - [N06000163]	08/2009	2,661.73 - 2,661.73	5,146.48	08/2019 -	-	93.35
	<u>Neyveli Lignite Corporation</u>						
7	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 - 17,237.00	17,237.80	11/2021 -	07/2022	.00
	<u>Singareni Colliers Company Limited</u>						
8	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 - 418.97	489.62	03/2012 -	03/2023	16.86

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(April 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
9	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	05/2015	397.09 - 397.09	442.42	03/2019 -	03/2022	11.42
10	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 - 447.06	473.22	03/2015 -	03/2023	5.85
11	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 - 162.76	349.28	03/2015 -	03/2022	114.60
	<u>Western Coal Fields Limited</u>						
12	BHANEGAON OC - [N06000121]	02/2015	187.94 - 187.94	409.68	03/2023 -	03/2023	117.98
13	NEW MAJRI UG TO OC - [N06000128]	05/2015	295.56 - 295.56	496.38	03/2019 -	09/2026	67.95
14	ADASA UG TO OC - [N06000133]	08/2015	288.90 - 288.90	333.43	03/2023 -	03/2024	15.41
15	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]	02/2016	198.68 - 198.68	325.18	03/2019 -	03/2022	63.67
16	BHATADI EXPANSION OC MINE - [N06000150]	02/2016	304.52 - 304.52	729.86	03/2019 -	09/2026	139.68
17	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	08/2016	319.76 - 319.76	404.45	03/2022 -	03/2022	26.49
18	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]	09/2016	289.29 - 289.29	289.30	03/2022 -	03/2025	.00
19	KOLAR PIMPRI EXTENSION OC - [N06000160]	03/2017	362.73 - 362.73	402.90	03/2020 -	09/2022	11.07
	Total		23,571.99 .00 23,571.99	27,530.00			
	<u>DPIIT</u>						
	<u>Delhi Mumbai Industrial Corridor</u>						
20	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]	09/2011	12,579.09 - 12,579.09	13,812.30	09/2019 -	07/2021	9.80
	<u>India International Convention And Expo Centre</u>						
21	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]	11/2017	4,773.00 - 4,773.00	5,178.00	12/2019 -	12/2021	8.49

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(April 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	Total		17,352.09 - 17,352.09	18,990.30			
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Central Public Works Department</u>						
22	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030	03/2019	1,577.00 - 1,577.00	1,828.00	09/2025 -	09/2025	15.92
	<u>Hospital Services Consultancy Corporation Ltd</u>						
23	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003	02/2013	414.11 - 414.11	499.23	11/2013 -	05/2021	20.55
24	AIIMS - MOTHER AND CHILD BLOCK - [N21000008	12/2013	204.44 - 204.44	250.00	05/2017 -	03/2021	22.29
25	AIIMS - OPD(NEW) - [N21000009	08/2014	293.65 - 293.65	325.00	05/2017 -	01/2020	10.68
26	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010	12/2014	168.90 - 168.90	191.20	05/2017 -	07/2019	13.20
27	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011	09/2014	505.58 - 505.58	585.00	03/2018 -	09/2019	15.71
28	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012	07/2016	152.95 - 152.95	177.92	02/2018 -	03/2021	16.33
29	CNCI KOLKATA WEST BENGAL - [N21000015	08/2016	244.00 - 244.00	248.00	09/2018 -	05/2019	1.64
30	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017	08/2017	272.19 - 272.19	272.54	03/2019 -	03/2021	.13
31	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019	12/2017	156.56 - 156.56	190.34	- -	06/2021	21.58
32	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022	01/2018	249.01 - 249.01	249.07	- -	01/2021	.02
	<u>National Building Construcion Corporation Ltd</u>						
33	AIIMS BILASPUR - [N21000028	04/2018	1,351.00 - 1,351.00	1,471.00	09/2021 -	09/2021	8.88
	Total		5,589.39 - 5,589.39	6,287.30			

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(April 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>HOME AFFAIRS</u>						
	<u>Central Public Works Department</u>						
34	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 - 1,219.21	2,000.00	10/2019 -	12/2021	64.04
	Total		1,219.21 .00 1,219.21	2,000.00			
	<u>HUMAN RESOURCE DEVELOPMENT</u>						
35	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100	02/2016	496.18 496.00 496.00	498.99	06/2017 -	10/2021	.60
36	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102	08/2016	294.00 - 294.00	350.69	04/2019 -	05/2021	19.28
37	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119	12/2016	549.31 - 549.31	559.47	07/2019 -	-	1.85
38	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133	02/2019	186.00 199.00 199.00	205.00	09/2020 -	-	3.02
	<u>Rail India Technical And Economic Service</u>						
39	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001	09/2013	484.32 - 484.32	626.26	09/2014 -	-	29.31
	Total		2,009.81 695.00 2,022.63	2,240.41			
	<u>PETROLEUM</u>						
	<u>Hindustan Petroleum Corporation Limited</u>						
40	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296	09/2017	2,677.00 - 2,677.00	3,072.00	06/2021 -	08/2022	14.76
	<u>Indian Oil Corporation Limited</u>						
41	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236	06/2016	423.00 - 423.00	502.00	08/2019 -	06/2021	18.68
	<u>Oil & Natural Gas Corporation Limited</u>						
42	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128	03/2011	861.79 - 1,846.46	2,001.00	05/2013 -	02/2022	132.19
	<u>Oil India Limited</u>						

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above (April 2021)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
43	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 - 352.56	490.24	03/2017 -	-	39.05
44	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	01/2018	543.91 - 543.91	652.10	02/2020 -	06/2021	19.89
	Total		4,858.26 .00 5,842.93	6,717.34			
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
45	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 - 11,638.55	15,105.22	01/2018 -	-	29.79
46	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	09/2014	9,188.98 - 9,188.98	9,842.02	07/2019 -	03/2021	7.11
47	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 - 14,366.58	15,389.42	06/2019 -	10/2022	7.12
48	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]	04/2012	9,750.89 - 9,750.89	12,176.28	02/2017 -	-	24.87
49	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 - 11,846.00	12,739.82	10/2017 -	-	7.55
50	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	07/2012	1,527.00 - 1,527.00	1,801.07	08/2017 -	-	17.95
51	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	03/2015	9,870.51 - 9,870.51	11,148.86	01/2020 -	-	12.95
52	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00 4,238.00	4,552.00	10/2017 -	-	7.41
	<u>Power Grid Corporation Of India Limited</u>						
53	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 - 203.28	260.03	07/2017 -	-	27.92
54	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 - 487.49	639.46	06/2014 -	-	31.17
55	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	03/2017	3,500.00 3,500.00 3,500.00	3,994.00	07/2020 -	06/2021	14.11
	<u>Satluj Jal Vidyut Nigam Limited</u>						

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(April 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
56	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 - 648.33	947.89	12/2021 -	12/2021	46.20
	<u>Thdc India Limited</u>						
57	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 - 2,491.58	3,860.35	06/2013 -	12/2023	54.94
	Total		79,757.15 7,738.00 79,757.19	92,456.42			
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
58	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89 - 792.89	1,377.48	03/2021 -	03/2023	73.73
59	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 - 184.06	315.00	03/2019 -	-	71.14
60	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 - 2,271.50	4,517.49	03/2021 -	03/2023	98.88
61	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 - 2,425.00	5,341.68	03/2024 -	03/2024	120.28
62	VAIBHAVWADI-KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 - 2,750.00	3,438.51	03/2024 -	03/2024	25.04
63	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	1,272.19 - 1,272.19	1,283.49	03/2022 -	03/2023	.89
64	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	02/2015	3,627.47 3,627.00 3,627.00	3,627.47	03/2024 -	03/2023	.01
65	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 - 1,876.00	2,081.27	03/2023 -	03/2023	10.94
	<u>Container Corporation Of India</u>						
66	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]	01/2013	387.70 - 387.70	487.13	03/2018 -	-	25.65
67	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 - 234.50	235.00	03/2019 -	-	.21
	<u>East Central Railways</u>						
68	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	03/1999	1,033.07 - 1,033.07	3,550.00	- -	03/2022	243.64

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(April 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
69	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	04/2003	528.65 - 528.65	2,066.78	- -	03/2023	290.95
70	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	477.88 283.95 283.95	751.55	03/2012 -	07/2021	164.68
71	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	324.73 - 324.73	1,070.00	03/2012 -	11/2022	229.50
72	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 - 162.87	614.45	- -	12/2023	277.26
73	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	499.41 - 499.41	516.02	03/2020 -	-	3.33
74	SAMASTIPUR-DARBANGHA - [N22000329]	05/2015	380.00 - 380.00	519.33	- -	03/2025	36.67
75	HAJIPUR - BACHAWARA - [N22000334]	05/2015	678.54 - 678.54	929.86	03/2019 -	05/2021	37.04
76	KODERMA-TILAIYA (NL), ECR - [220100305]	04/2002	459.91 - 459.91	1,625.87	- -	03/2023	253.52
77	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 - 415.67	549.75	- -	-	32.26
78	BIHTA-AURANGABAD (NL) - [N22000170]	04/2008	326.20 - 326.20	2,995.01	- -	03/2024	818.15
79	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	325.00 - 325.00	735.20	- -	03/2021	126.22
80	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	378.56 - 378.56	1,858.75	- -	03/2023	391.01
81	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 - 211.00	1,006.00	- -	-	376.78
82	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]	04/2004	372.14 - 372.14	1,470.50	- -	03/2023	295.15
83	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]	04/2009	548.00 - 548.00	819.01	03/2020 -	03/2023	49.45
84	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 - 213.01	480.00	- -	-	125.34

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(April 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
85	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 - 332.15	546.71	07/2014 -	-	64.60
86	SAGALI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 - 744.04	1,215.54	03/2021 -	03/2024	63.37
87	MUZAFFARPUR SAGALI DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 - 731.64	1,185.73	03/2021 -	06/2022	62.06
88	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]	04/1998	180.82 - 180.82	726.31	- -	-	301.68
89	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]	04/1991	329.39 - 329.39	1,483.14	- -	03/2022	350.27
	<u>East Coast Railway</u>						
90	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	1,111.99 - 1,111.99	1,539.28	02/2019 -	12/2021	38.43
91	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	04/2015	701.61 - 701.61	810.02	11/2018 -	03/2024	15.45
	<u>Eastern Railways</u>						
92	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 - 1,188.91	1,619.48	03/2019 12/2009	03/2025	36.22
93	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 - 607.09	1,425.44	02/2013 -	03/2024	134.80
94	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]	04/2010	365.17 - 365.17	439.30	03/2017 -	03/2025	20.30
95	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 - 365.17	527.54	- -	03/2025	44.46
96	HANSDIHA-GODDA NL - [N22000236]	04/2011	542.18 - 542.18	663.13	03/2020 -	03/2021	22.31
97	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]	04/2011	175.80 - 175.80	495.10	- -	03/2022	181.63
98	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	04/2011	299.60 - 299.60	335.62	03/2017 -	03/2026	12.02
99	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]	04/2010	494.54 - 494.54	494.59	03/2005 -	03/2025	.01

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(April 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
100	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241	04/2000	297.47 - 297.47	298.22	- -	03/2025	.25
101	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243	04/2009	499.96 - 499.96	680.68	02/2012 -	03/2025	36.15
102	MONIGRAM- NIMTITA - [N22000301	04/2012	250.93 - 250.93	310.70	- -	03/2024	23.82
103	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302	04/2012	255.64 - 255.64	272.20	- -	03/2022	6.48
104	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216	04/1987	406.99 - 406.99	545.70	03/2006 -	03/2025	34.08
105	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217	04/2007	450.00 - 450.00	1,261.34	- -	03/2025	180.30
106	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218	04/2010	172.03 - 172.03	260.10	- -	03/2025	51.19
107	PIRPAINTI-JASIDIH - [N22000219	04/2013	915.98 - 915.98	2,137.81	03/2022 -	03/2025	133.39
108	BANDEL-BOINCHI 3RD LINE - [N22000221	04/2011	288.35 - 288.35	502.48	- -	03/2021	74.26
109	PIRPAINTI-BHAGALPUR - [N22000222	04/2011	261.38 - 261.38	565.00	- -	05/2019	116.16
110	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224	04/2001	923.52 - 923.52	995.10	03/2016 -	03/2025	7.75
111	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225	04/2005	595.51 - 595.51	769.40	03/2017 -	03/2025	29.20
<u>Indian Railway Construction Company Limited</u>							
112	GEVRA ROAD PENDRA ROAD - [N22000488	02/2014	2,288.00 - 2,288.00	4,970.11	03/2022 -	12/2023	117.23
113	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489	04/2013	3,055.00 - 3,055.00	3,055.15	09/2018 -	03/2022	.00
<u>Metropolitan Rapid Transport Projects</u>							
114	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69 - 1,049.69	3,404.92	12/2006 -	-	224.37

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(April 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
115	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 - 495.44	2,980.41	03/2004 -	03/2022	501.57
116	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 - 495.74	734.01	06/2013 -	12/2021	48.06
117	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	03/2013	4,874.58 - 4,874.58	8,574.97	03/2016 -	06/2021	75.91
<u>North Central Railway</u>							
118	ETAWAH-MAINPURI (NL),NCR - [220100318]	04/1997	120.00 - 120.00	346.00	12/2008 -	-	188.33
119	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96 - 2,912.96	3,845.60	03/2022 -	12/2024	32.02
120	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	04/2015	668.70 668.00 668.00	680.00	03/2020 -	-	1.80
<u>North East Frontier Railway</u>							
121	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	297.32 - 200.34	614.00	03/2019 -	-	106.51
122	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 - 5,021.45	5,521.45	03/2014 -	03/2023	130.69
123	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	1,180.19 - 2,531.34	4,541.38	12/2008 -	05/2021	284.80
124	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 - 4,454.17	12,264.15	03/2011 -	12/2023	175.34
125	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	385.20 - 385.20	1,043.00	03/2019 -	03/2023	170.77
126	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	532.87 - 2,132.03	2,145.00	03/2019 -	03/2024	302.54
127	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	2,326.52 - 2,326.52	6,911.00	03/2015 -	12/2024	197.05
128	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	333.76 - 333.76	360.00	- -	-	7.86
129	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 - 1,339.48	8,600.00	12/2015 -	-	542.04

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(April 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
130	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 - 221.42	380.00	- -	-	71.62
131	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 - 569.63	742.00	03/2020 -	03/2022	30.26
132	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	906.46 - 1,202.33	4,083.02	03/2021 -	-	350.44
133	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 - 242.22	471.00	03/2020 -	-	94.45
134	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 - 241.52	373.87	- -	12/2021	54.80
135	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84 - 414.84	1,040.00	03/2020 -	-	150.70
136	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	04/1999	819.23 - 819.23	1,871.00	- -	-	128.39
137	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	314.00 - 486.96	800.00	03/2019 -	03/2021	154.78
138	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	04/2015	2,232.32 - 2,232.32	2,950.00	03/2022 -	03/2023	32.15
139	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 - 870.96	1,873.21	03/2021 -	05/2021	115.07
140	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) [N22000390]	04/2016	602.27 - 602.27	2,144.78	12/2021 -	04/2021	256.12
141	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHOWA-JAIN - [N22000499]	02/1999	380.60 - 380.60	1,090.60	04/2010 -	-	186.55
<u>North Eastern Railway</u>							
142	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	142.45 - 142.45	228.40	- -	-	60.34
143	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 - 182.92	197.73	- -	-	8.10
144	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 - 307.00	1,409.09	- -	-	358.99
145	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 - 243.78	895.00	12/2021 -	12/2021	267.13

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(April 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
146	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 - 295.00	477.31	01/2019 -	02/2022	61.80
147	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 - 643.00	644.00	- -	-	.16
148	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 - 213.00	213.35	04/2016 -	12/2021	.16
149	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]	04/2017	1,343.00 - 1,343.00	1,476.15	01/2018 -	-	9.91
150	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]	04/2016	602.50 - 602.50	714.34	- -	12/2023	18.56
	<u>North Western Railway</u>						
151	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 - 410.08	860.41	02/2019 -	06/2022	109.82
152	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 - 600.00	701.81	03/2020 -	10/2022	16.97
153	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL [N22000330]	05/2015	873.71 - 873.71	1,980.21	- -	-	126.64
154	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 - 246.08	395.00	12/2019 -	02/2021	60.52
155	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 - 2,082.75	4,262.36	- -	-	104.65
156	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 - 236.93	350.45	10/2018 -	01/2020	47.91
157	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]	04/2013	822.00 - 822.00	1,099.00	- -	-	33.70
158	PUSHKAR-MERTA - [N22000151]	04/2013	323.00 - 323.00	432.22	- -	-	33.81
159	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR [N22000152]	04/2013	420.18 - 420.18	480.00	03/2020 -	06/2021	14.24
160	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 - 213.39	375.00	11/2019 -	03/2021	75.73
161	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 - 242.09	525.00	02/2019 -	02/2020	116.86

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above (April 2021)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>Northern Railway</u>						
162	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 - 156.65	359.00	- -	03/2024	129.17
163	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 - 287.00	893.45	12/2011 -	06/2021	211.31
164	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]	04/2007	336.91 - 336.91	791.39	- -	03/2023	134.90
165	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]	04/2012	295.68 - 295.68	419.00	- -	09/2023	41.71
166	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 - 219.83	346.63	- -	-	57.68
167	UNCHAHAH-AMETHI - [N22000294]	04/2012	1,229.00 - 1,229.00	1,265.00	- -	03/2023	2.93
168	QADIAN-BEAS - [N22000295]	04/2011	205.22 - 205.22	841.90	- -	03/2024	310.24
169	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 - 450.00	2,200.00	07/2012 -	03/2024	388.89
170	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 - 2,500.00	27,949.00	11/2002 -	12/2022	1,017.96
171	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 - 625.00	859.00	03/2016 -	06/2021	37.44
	<u>Rail Vikas Nigam Ltd.</u>						
172	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	1,185.64 - 1,185.64	1,844.47	12/2017 -	-	55.57
173	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	1,202.70 - 1,202.70	2,440.53	02/2015 -	06/2022	102.92
174	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00 207.00	396.00	03/2009 03/2009	-	91.30
175	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	04/2010	2,913.51 - 2,913.51	4,639.00	03/2016 -	03/2025	59.22
176	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	2,966.99 - 2,966.99	6,753.42	12/2026 -	12/2025	127.62

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(April 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
177	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 - 2,127.00	3,000.00	03/2023 -	12/2022	41.04
178	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 - 3,951.98	4,259.48	03/2016 -	03/2025	7.78
179	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 - 2,298.42	2,733.86	03/2014 -	12/2025	18.95
180	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]	03/2012	1,503.71 - 1,503.71	3,377.00	03/2020 -	03/2022	124.58
181	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	975.62 - 975.62	1,500.00	12/2021 -	12/2021	53.75
182	DHASA-JETALSAR (GC) - [N22000141]	04/2012	644.38 - 644.38	872.65	03/2021 -	03/2021	35.42
183	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	04/2013	1,548.66 - 1,548.66	1,868.89	12/2021 -	03/2022	20.68
184	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 - 632.68	950.00	03/2016 -	12/2021	50.15
185	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 - 3,246.26	3,548.68	12/2023 -	12/2023	9.32
186	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	943.60 - 943.60	1,000.00	03/2022 -	12/2024	5.98
187	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	04/2015	773.94 - 773.94	850.00	12/2024 -	12/2024	9.83
188	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 - 927.01	1,400.00	03/2019 -	06/2022	51.02
189	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	04/2011	16,216.00 - 16,216.00	22,716.11	12/2024 -	03/2025	40.08
190	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 - 713.48	2,725.00	03/2020 -	12/2021	281.93
191	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 - 2,335.67	3,327.72	12/2024 -	12/2026	42.47
192	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 - 948.04	2,009.00	03/2020 -	12/2021	111.91

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(April 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
193	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 - 942.95	1,536.00	03/2019 -	06/2022	62.89
194	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	03/2012	1,183.25 - 1,183.25	1,825.00	12/2020 -	12/2022	54.24
195	BINA - KOTA DOUBLING WITH RE - [N22000414]	04/2011	1,485.85 - 1,485.85	1,835.83	12/2020 -	12/2021	23.55
	<u>Railway Electrification</u>						
196	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 - 171.10	275.08	03/2012 -	-	60.77
	<u>South Central Railway</u>						
197	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 - 1,045.20	2,120.16	03/2009 -	03/2024	102.85
198	MANUGURU-RAMAGUNDAM - [N22000259]	04/2013	1,112.00 - 1,112.00	2,911.84	- -	-	161.86
199	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	04/2012	1,856.95 - 1,856.95	1,952.68	03/2023 -	03/2024	5.16
200	NADIKUDE-SRI KALAHASTI - [N22000286]	04/2011	2,288.70 - 2,288.70	2,643.25	03/2021 -	03/2024	15.49
201	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	704.31 - 704.31	927.94	03/2020 -	06/2021	31.75
202	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]	04/2008	2,132.77 - 2,132.77	3,037.95	03/2014 -	03/2027	42.44
203	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	164.36 - 164.36	1,050.00	02/2009 -	-	538.84
204	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	1,723.00 1.00 1.00	3,421.35	03/2000 -	03/2023	3,42,035.00
205	GUNTUR-GUNTAKAL - [N22000368]	04/2016	3,631.00 - 3,631.00	3,887.48	03/2022 -	03/2024	7.06
206	MANMAD-PARBHANI-NANDED-SECUNDERABAD- GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	04/2017	119.73 185.00 185.00	449.39	03/2022 -	12/2022	142.91
	<u>South East Central Railway</u>						
207	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 - 383.79	1,413.76	- -	-	268.37

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above (April 2021)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
208	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	511.86 - 511.86	2,005.25	04/2020 -	-	291.76
209	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,908.51 - 1,908.51	3,524.81	03/2023 -	12/2023	84.69
210	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438]	04/2010	585.93 - 585.93	1,268.32	02/2019 -	12/2021	116.46
211	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00 - 229.00	1,096.00	12/2021 -	12/2024	378.60
212	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]	04/2008	872.00 - 872.00	1,226.51	12/2019 -	-	40.65
213	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	04/2015	1,973.00 - 1,973.00	2,135.34	03/2021 -	12/2023	8.23
214	ANUPPUR-KATNI - [N22000485]	04/2015	1,370.00 - 1,370.00	1,370.94	12/2021 -	12/2023	.07
<u>South Eastern Railway</u>							
215	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30 154.30	1,026.00	03/2007 03/2007	-	564.94
216	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 - 148.77	377.00	12/2016 -	08/2020	153.41
217	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 - 267.37	620.00	- -	03/2025	131.89
218	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	651.00 - 651.00	1,009.00	03/2015 -	03/2025	54.99
219	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 - 149.90	230.00	03/2015 -	-	53.44
220	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 - 1,966.70	2,373.00	03/2003 -	03/2030	130.97
<u>South Western Railway</u>							
221	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	1,801.01 - 1,801.01	1,967.00	- -	12/2023	9.22
222	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 - 296.00	296.10	- -	12/2023	.03

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(April 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
223	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	2,062.30 - 2,062.30	2,432.50	- -	03/2025	17.95
224	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 - 146.75	167.50	- -	12/2023	14.14
225	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	2,315.00 - 2,315.00	3,911.65	- -	12/2024	68.97
226	HUBLI- CHIKJAJUR - [N22000325]	03/2015	1,156.94 - 1,156.94	1,656.00	03/2020 -	03/2023	43.14
227	YELAHANKA-PENUKONDA - [N22000328]	05/2015	860.43 - 860.43	1,147.00	03/2020 -	06/2021	33.31
228	ARSIKERE-TUMKUR - [N22000332]	03/2015	578.00 - 578.00	783.00	03/2020 -	06/2021	35.47
229	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 - 1,614.59	1,870.41	03/2019 -	03/2024	15.84
230	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78 - 644.78	998.00	03/2017 -	03/2025	54.78
	<u>Southern Railway</u>						
231	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY'-AGASTIYAMPALLI [N22000079]	09/2007	724.69 - 724.69	2,910.84	02/2019 -	03/2025	301.67
232	TIRUCHIRAPPALI-NAGORE-KARAIKAL(SR)(GC) - [220100262]	09/1995	303.98 - 303.98	1,720.00	03/2020 -	03/2025	465.83
233	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	1,566.00 - 1,566.00	2,815.62	- -	-	79.80
234	ATTIPPATTU PUTTUR - [N22000184]	04/2008	151.84 - 151.84	527.37	02/2019 -	-	247.32
235	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 - 523.52	1,205.00	- -	03/2024	130.17
236	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 - 839.00	1,500.00	- -	-	78.78
237	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 - 198.68	559.95	- -	03/2024	181.84
238	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 - 270.14	457.08	- -	12/2021	69.20

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(April 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
239	KUMBALAM-TURAVUR - [N22000191]	04/2011	252.96 - 252.96	369.55	- -	-	46.09
240	ERODE-PALANI - [N22000199]	04/2008	288.57 - 288.57	1,140.00	- -	-	295.05
241	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 - 164.41	608.13	- -	09/2021	269.89
242	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	931.98 - 931.98	1,121.00	- -	05/2021	20.28
243	ERNAKULAM-KUMBALAM - [N22000204]	04/2010	189.24 - 189.24	275.21	- -	-	45.43
244	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70 - 120.70	2,172.16	03/2019 -	12/2027	1,699.64
245	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]	10/2013	187.26 - 187.26	327.00	04/2014 -	-	74.62
246	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]	02/2015	1,000.00 - 1,000.00	1,246.00	- -	-	24.60
247	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	02/1996	268.87 - 268.87	950.00	03/2005 -	09/2021	253.33
248	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00 - 760.00	1,536.00	03/2020 -	06/2022	102.11
<u>West Central Railway</u>							
249	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60 - 424.60	2,909.99	03/2021 -	03/2023	585.35
250	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 - 247.66	8,248.50	05/2008 -	03/2025	3,230.57
<u>Western Railway</u>							
251	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]	04/2006	117.36 196.95 196.95	202.35	03/2011 -	-	2.74
Total			1,88,639.64 5,323.20 1,93,962.84	3,76,212.69			
<u>ROAD TRANSPORT AND HIGHWAYS</u>							
<u>Ministry Of Road Transport And Highways (State Pwds)</u>							

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(April 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
252	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276	12/2011	156.26 227.00 227.00	247.95	- -	-	9.23
253	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306	11/2010	624.41 - 624.41	992.67	03/2011 -	-	58.98
254	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308	08/2010	193.69 - 193.69	327.92	10/2010 -	06/2021	69.30
255	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311	03/2012	207.03 - 207.03	389.45	05/2012 -	-	88.11
256	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316	03/2015	258.97 - 258.97	268.92	08/2015 -	-	3.84
257	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259	03/2015	280.16 - 280.16	290.59	- -	-	3.72
258	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00 348.00	348.43	09/2017 -	-	.12
259	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371	10/2013	445.89 - 445.89	653.29	03/2017 -	-	46.51
260	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388	11/2013	497.05 - 497.05	881.05	05/2017 -	-	77.26
261	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392	11/2010	268.08 - 268.08	390.73	05/2017 -	-	45.75
262	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391	11/2015	889.24 - 889.24	904.82	- -	-	1.75
263	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396	11/2010	470.20 - 470.20	630.36	02/2011 -	-	34.06
264	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398	01/1991	282.41 - 282.41	322.01	08/2016 -	-	14.02
265	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401	11/2011	954.43 - 954.43	1,191.51	09/2015 -	10/2021	24.84
266	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402	01/1991	358.22 - 358.22	377.64	10/2016 -	-	5.42
267	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407	10/2015	333.21 - 333.21	353.89	11/2015 -	-	6.21

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(April 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
268	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]	08/2010	195.04 - 195.04	377.99	10/2010 -	06/2021	93.80
269	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]	01/1991	319.68 - 319.68	369.77	- -	-	15.67
270	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]	06/2016	157.30 157.00 157.00	157.30	06/2018 -	-	.19
271	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]	03/2018	460.73 - 460.73	461.00	- -	-	.06
272	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]	11/2017	237.80 - 237.80	238.00	11/2019 -	-	.08
273	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]	03/2018	166.21 - 166.21	173.41	08/2018 -	-	4.33
274	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]	03/2018	217.22 - 217.22	226.88	08/2018 -	09/2021	4.45
275	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DSIGN CH0.0) TO KM 275/622(DSIGN CH 5.12 - [N24000928]	10/2015	333.21 - 333.21	355.89	12/2015 -	-	6.81
276	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (- [N24000938]	03/2018	297.12 294.00 294.00	294.12	07/2018 -	-	.04
277	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]	03/2018	504.19 504.00 504.00	504.19	11/2018 -	-	.04
278	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]	03/2016	995.09 995.00 995.00	995.09	05/2016 -	-	.01
279	KHAMGAON TO SHEGAON - [N24001009]	02/2017	203.21 203.00 203.00	203.21	05/2019 -	-	.10
280	SHEGAON TO DEORI PHATA - [N24001010]	02/2017	373.10 373.00 373.00	373.10	05/2019 -	-	.03
281	MEHKAR TO CHIKALI - [N24001011]	02/2017	322.48 322.00 322.00	322.48	05/2019 -	-	.15
282	CHIKALI TO KHAMGAON - [N24001012]	02/2017	548.03 548.00 548.00	548.03	06/2019 -	-	.01
283	DIGRAS DARWAH KARANJA - [N24001013]	01/2017	391.06 391.00 391.00	391.06	06/2019 -	-	.02

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(April 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
284	MORSHI TO ACHALPUR - [N24001015]	01/2017	341.16 341.00 341.00	341.16	06/2019 -	-	.05
285	KARAD TO VITA - [N24001049]	01/2018	344.85 245.00 245.00	344.85	12/2019 -	-	40.76
286	SANGOLA TO JATH - [N24001052]	01/2018	257.38 257.00 257.00	257.38	12/2019 -	-	.15
287	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]	02/2017	422.02 422.00 422.00	422.02	07/2019 -	-	.00
288	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]	02/2017	407.19 407.00 407.00	407.19	06/2019 -	-	.05
289	PALPHATA TO PHULAMBARA - [N24001060]	03/2018	227.19 227.00 227.00	227.19	12/2019 -	-	.08
290	CHIKALI TO DHAD - [N24001061]	03/2018	189.46 189.00 189.00	189.46	12/2019 -	-	.24
291	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]	03/2018	336.21 336.00 336.00	336.21	12/2019 -	-	.06
292	WADIGODRI TO DHANGRIIMPRI - [N24001063]	03/2018	194.23 194.00 194.00	194.23	02/2020 -	-	.12
293	DHANGRIIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]	03/2018	217.14 217.00 217.00	217.14	02/2020 -	-	.06
294	PARBHANI TO GANGKHED - [N24001065]	03/2018	238.19 238.00 238.00	238.19	12/2019 -	-	.08
295	LATUR TO PANGAON - [N24001066]	03/2018	336.47 336.00 336.00	336.47	12/2019 -	-	.14
296	OMREGA TO AUSA - [N24001067]	03/2018	272.04 272.00 272.00	272.04	12/2019 -	-	.01
297	KOTHARI TO DHANORA - [N24001073]	09/2018	301.38 301.00 301.00	301.38	08/2020 -	-	.13
298	OSMANNAGAR TO KUNDRAL - [N24001075]	09/2017	344.25 344.00 344.00	344.25	08/2020 -	-	.07
299	KUNDRAL TO WAZAR - [N24001077]	01/2018	225.25 225.00 225.00	225.25	12/2019 -	-	.11

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(April 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
300	ARDHAPUR TO HIMAYATNAGAR - [N24001079]	12/2017	426.06 426.00 426.00	426.06	06/2020 -	-	.01
301	CHIKLI TO TAKARKHED - [N24001083]	03/2018	393.10 393.00 393.00	393.10	12/2019 -	-	.03
302	MANGRUPHIR TO MAHAN - [N24001087]	03/2018	222.13 222.00 222.00	222.13	11/2019 -	-	.06
303	JALGAON TO NANDURA - [N24001088]	03/2018	177.84 177.00 177.00	177.84	12/2019 -	-	.47
304	MALEGAON TO RISOD - [N24001089]	02/2018	303.24 303.00 303.00	303.24	12/2019 -	-	.08
305	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]	03/2016	536.65 356.00 356.00	536.65	12/2019 -	06/2021	50.74
306	NAIGAONBANDI TO MANGRULPIR - [N24001094]	12/2017	244.04 244.00 244.00	244.04	03/2019 -	-	.02
307	TALEGAON TO GONAPUR - [N24001096]	01/2018	264.41 264.00 264.00	264.41	03/2019 -	-	.16
308	SELDOH TO PANVAR - [N24001097]	07/2018	404.33 404.00 404.00	404.33	05/2020 -	-	.08
309	PANCHARAL TO MANDANGHAR - [N24001107]	07/2018	381.08 302.00 302.00	381.08	05/2020 -	-	26.19
310	VADPALE TO BHOGAN KHURD - [N24001115]	01/2017	1,598.47 1,560.00 1,560.00	1,598.47	11/2019 -	-	2.47
311	BHOKAR TO SARSAM - [N24001128]	02/2017	295.09 - 295.09	295.99	07/2019 -	-	.31
312	BHOGAN KHURD TO KASHEDI - [N24001132]	09/2017	743.21 743.00 743.00	743.21	06/2021 -	06/2021	.03
313	PARSHURAM GHAT TO ARAWALI - [N24001133]	04/2016	983.14 983.00 983.00	983.14	12/2019 -	-	.01
314	KANTE TO WAKED - [N24001134]	03/2016	1,230.02 1,230.00 1,230.00	1,230.02	11/2019 -	-	.00
315	KALMATH TO ZARAP - [N24001137]	09/2016	1,338.13 1,338.00 1,338.00	1,338.13	03/2020 -	-	.01

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(April 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
316	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]	11/2016	215.16 215.00 215.00	215.16	09/2019 -	-	.07
317	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]	03/2016	240.30 240.00 240.00	240.30	01/2020 -	03/2021	.13
318	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH - [N24001144]	10/2013	445.89 653.00 653.00	653.29	03/2017 -	04/2021	.04
319	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]	08/2010	186.96 - 186.96	322.24	09/2014 -	06/2021	72.36
320	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]	09/2011	1,979.00 - 1,979.00	2,036.90	- -	-	2.93
321	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]	01/2016	476.20 544.00 543.73	544.00	09/2016 -	06/2021	.00
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
322	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]	02/2017	195.23 - 195.23	252.79	04/2017 -	-	29.48
323	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]	02/2017	203.36 - 203.36	263.31	04/2017 -	-	29.48
324	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]	01/2017	194.66 - 194.66	252.05	04/2017 -	-	29.48
325	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]	03/2016	373.07 - 373.07	387.00	08/2016 -	05/2021	3.73
326	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]	01/2017	198.22 - 198.22	252.05	04/2017 -	-	27.16
327	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]	04/2017	388.00 - 388.00	447.37	10/2017 -	-	15.30
328	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]	10/2017	818.00 - 818.00	887.68	- -	-	8.52
	<u>National Highways Authority Of India</u>						
329	HARANGAJAO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 - 280.00	520.00	02/2009 -	-	85.71
330	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 - 199.81	340.14	04/2009 -	-	70.23

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(April 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
331	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279	12/2003	167.64 - 167.64	435.78	11/2008 -	-	159.95
332	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 - 155.04	255.23	11/2008 -	-	64.62
333	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049	12/2003	160.00 - 160.00	167.98	05/2008 -	06/2019	4.99
334	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 - 196.00	655.17	07/2009 -	-	234.27
335	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 - 1,108.00	2,967.50	11/2011 -	-	167.82
336	INDORE-DEWAS(NH-3) - [N24000159	11/2010	325.00 - 325.00	475.00	05/2013 -	-	46.15
337	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063	12/2003	217.61 - 217.61	360.84	04/2010 -	07/2019	65.82
338	NALBARI T BIJNI (AS-7) - [N24000048	12/2003	208.00 - 208.00	230.00	04/2008 -	02/2021	10.58
339	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233	04/2014	1,266.60 - 1,266.60	1,544.00	09/2016 -	-	21.90
340	NASHRI- CHANANI - [N24000162	05/2011	2,159.00 - 2,159.00	2,519.00	06/2015 -	-	16.67
341	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182	09/2011	2,848.00 - 2,848.00	3,379.45	03/2014 -	12/2022	18.66
342	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188	05/2011	511.54 - 585.00	591.00	11/2013 -	01/2021	15.53
343	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224	10/2012	1,928.22 - 1,928.22	3,182.34	04/2015 -	06/2021	65.04
344	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435	10/2015	531.13 - 531.13	730.97	05/2018 -	06/2021	37.63
345	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437	10/2015	361.15 - 361.15	363.93	- -	-	.77
346	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441	10/2015	593.26 - 593.26	690.17	05/2018 -	06/2021	16.34

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(April 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
347	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]	06/2015	845.24 - 845.24	941.00	- -	-	11.33
348	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) [N24000463]	12/2015	1,083.00 - 1,083.00	1,827.15	06/2018 -	-	68.71
349	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]	03/2015	794.30 - 679.94	691.38	- -	05/2020	-12.96
350	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]	08/2015	814.04 - 814.04	825.17	- -	10/2021	1.37
351	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	05/2013	1,055.00 - 1,055.00	1,601.77	11/2015 -	-	51.83
352	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]	10/2015	447.29 - 447.29	746.43	12/2017 -	-	66.88
353	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]	01/1991	642.41 - 642.41	681.67	- -	-	6.11
354	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]	12/2015	1,167.45 - 1,167.45	1,182.94	- -	-	1.33
355	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]	04/2014	1,665.00 - 1,665.00	2,360.65	- -	-	41.78
356	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]	08/2015	854.80 - 854.80	1,038.56	- -	-	21.50
357	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]	08/2015	516.13 - 516.13	649.27	04/2018 -	-	25.80
358	MEERUT-BULANDSHAHAH - [N24000539]	01/2016	683.24 - 683.24	987.94	- -	-	44.60
359	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]	02/2016	997.15 - 997.15	1,115.95	03/2019 -	-	11.91
360	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 TO 208.300 KM [PACKAGE-IV] [N24000551]	03/2016	1,587.49 - 1,587.49	2,982.00	04/2019 -	-	87.84
361	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]	05/2016	364.56 - 364.56	392.00	- -	04/2021	7.53
362	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- [N24000594]	07/2016	458.03 - 458.03	486.00	- -	-	6.11

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(April 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
363	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600	08/2016	1,388.34 - 1,388.34	2,587.50	09/2019 -	-	86.37
364	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601	08/2016	1,169.61 - 1,169.61	2,280.00	- -	-	94.94
365	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607	08/2016	323.72 - 323.72	336.60	08/2018 -	-	3.98
366	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621	09/2016	1,239.82 - 1,239.82	1,727.66	- -	-	39.35
367	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622	09/2016	950.69 - 950.69	1,108.00	08/2019 -	-	16.55
368	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623	09/2016	1,100.19 - 1,100.19	1,145.31	- -	03/2021	4.10
369	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631	11/2016	290.73 - 290.73	315.00	- -	-	8.35
370	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638	11/2012	605.84 - 605.84	722.46	07/2018 -	-	19.25
371	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.71 - 1,184.71	1,310.00	03/2020 -	-	10.58
372	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	03/2017	744.64 - 744.64	982.00	03/2020 -	-	31.88
373	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657	03/2017	1,030.44 - 1,030.44	1,065.51	03/2020 -	-	3.40
374	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	03/2017	988.34 - 988.34	1,043.28	03/2020 -	-	5.56
375	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659	03/2017	1,059.73 - 1,059.73	1,071.00	03/2017 -	-	1.06
376	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	03/2017	1,098.06 - 1,098.06	1,160.64	03/2020 -	-	5.70
377	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	03/2017	754.54 - 754.54	756.27	03/2020 -	12/2021	.23
378	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	03/2017	672.89 - 672.89	736.01	03/2020 -	-	9.38

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(April 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
379	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 - 1,041.62	1,187.10	03/2020 -	-	13.97
380	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 - 1,288.07	1,420.00	03/2020 -	06/2021	10.24
381	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 - 2,064.99	2,447.00	03/2020 -	-	18.50
382	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 - 831.58	1,177.00	03/2020 -	-	41.54
383	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 - 993.16	1,434.00	03/2020 -	-	44.39
384	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691	04/2017	894.00 - 894.00	929.32	04/2020 -	07/2021	3.95
385	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693	06/2017	1,958.88 - 1,958.88	1,993.81	06/2020 -	02/2021	1.78
386	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704	09/2017	1,124.11 - 1,124.11	1,232.76	09/2017 -	05/2021	9.67
387	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713	12/2017	404.94 - 404.94	448.18	- -	10/2020	10.68
388	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725	01/2018	273.46 - 273.46	276.17	- -	-	.99
389	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784	02/2018	1,424.77 - 1,424.77	1,853.42	- -	-	30.09
390	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785	02/2018	1,166.26 - 1,166.26	1,296.93	- -	08/2021	11.20
391	SIX-LANING OF BANGALORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787	02/2018	1,995.34 - 1,995.34	2,400.00	- -	11/2021	20.28
392	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789	02/2018	2,177.80 - 2,177.80	2,450.00	- -	-	12.50
393	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790	03/2018	1,261.98 - 1,261.98	1,952.20	- -	07/2021	54.69
394	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793	03/2018	925.40 - 925.40	1,197.00	- -	-	29.35

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(April 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
395	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800	03/2018	1,120.57 - 1,120.57	1,332.00	- -	-	18.87
396	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801	02/2018	1,052.21 - 1,052.21	1,449.00	- -	01/2021	37.71
397	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807	03/2018	1,532.62 - 1,532.62	2,499.00	03/2021 -	04/2021	63.05
398	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813	03/2018	496.20 - 496.20	537.17	- -	-	8.26
399	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814	03/2018	1,029.96 - 1,029.96	1,261.05	- -	03/2021	22.44
400	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829	03/2018	1,016.92 - 1,016.92	1,071.00	- -	01/2022	5.32
401	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830	03/2018	2,065.96 - 2,065.96	2,169.00	- -	-	4.99
402	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831	03/2018	1,294.47 - 1,294.47	1,296.00	- -	-	.12
403	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839	03/2018	634.70 - 634.70	931.21	- -	07/2021	46.72
404	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841	03/2018	795.50 - 795.50	799.30	- -	07/2021	.48
405	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853	03/2018	642.13 - 642.13	807.00	- -	-	25.68
406	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199	10/2019	743.88 - 743.88	743.89	- -	12/2021	.00
407	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212	12/2017	656.98 - 656.98	840.00	- -	11/2022	27.86
408	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214	12/2017	217.96 - 217.96	884.00	- -	-	305.58
	Total		1,07,225.71 19,510.00 1,07,213.14	1,32,093.27			
	TELECOMMUNICATIONS						
	Bharat Sanchar Nigam Limited						

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(April 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
409	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114	03/2020	431.16 431.00 431.00	431.16	06/2021 -	11/2021	.04
	<u>Department Of Telecommunication</u>						
410	NETWORK FOR SPECTRUM - [N26000101	03/2012	13,334.00 - 13,334.00	24,664.00	07/2015 -	07/2021	84.97
	Total		13,765.16 431.00 13,765.00	25,095.16			
	<u>URBAN DEVELOPMENT</u>						
	<u>Ahmedabad Metro Rail</u>						
411	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122	11/2014	10,773.00 - 10,773.00	12,787.00	12/2018 -	08/2022	18.69
	<u>Chennai Metro Rail Ltd</u>						
412	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084	02/2009	14,600.00 - 14,600.00	19,058.00	12/2015 -	-	30.53
	<u>Kochi Metro Rail Corporation Ltd</u>						
413	KOCHI METRO RAIL PROJECT - [N28000081	07/2012	5,181.79 - 5,181.79	6,218.14	07/2017 -	-	20.00
	<u>Mumbai Metro Rail Corporation Ltd</u>						
414	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086	07/2013	23,136.00 - 23,136.00	33,406.00	01/2015 -	03/2023	44.39
	<u>National Building Construcion Corporation Ltd</u>						
415	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080	06/2012	4,264.00 - 4,264.00	4,720.73	11/2019 -	-	10.71
	Total		57,954.79 .00 57,954.79	76,189.87			
	<u>WATER RESOURCES</u>						
	<u>Uttar Pradesh Jal Nigam</u>						
416	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021	01/2019	231.79 - 231.79	234.03	12/2021 -	12/2021	.97
417	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024	02/2019	681.78 - 681.78	690.71	06/2022 -	06/2022	1.31

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above (April 2021)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	Total		913.57 .00 913.57	924.74			
	Grand Total		5,31,616.04 33,697.20 5,39,737.47	8,08,948.83			

Details of Central Sector Projects Costing Rs.150 crore and above (as on					30.04.2021)
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	ARUNACHAL PRADESH				
	Power				
1	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009 (2/2021) [0/0]	2,496.90 (7,927.34) [7,927.34]	8,225.88 (5,430.44) [0]
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (8/2023) [8/2023]	6,285.33 (19,992.43) [19,992.43]	13,732.39 (13,707.10) [155]
	Road Transport And Highways				
3	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN	3/2015	/ (-) [0/0]	172.75 (-) [172.75]	134.38 (0.00) [0]
4	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	3/2015	6/2018 (-) [0/0]	394.00 (-) [394.00]	400.56 (0.00) [0]
5	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX	10/2015	/ (1/2016) [1/2019]	210.50 (210.50) [210.50]	145.07 (0.00) [0]
6	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST	11/2016	/ (-) [9/2020]	243.89 (-) [243.89]	145.31 (0.00) [0]
7	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1)	3/2019	2/2020 (-) [0/0]	403.68 (-) [403.68]	40.08 (0.00) [0]
8	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE	3/2019	11/2020 (-) [0/0]	543.05 (-) [543.05]	86.24 (0.00) [0]
9	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE	3/2019	11/2020 (-) [0/0]	450.65 (-) [450.65]	6.51 (0.00) [0]
10	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE	3/2019	10/2020 (-) [0/0]	486.70 (-) [486.70]	54.10 (0.00) [0]
11	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE	3/2019	2/2020 (-) [0/0]	560.39 (-) [560.39]	118.45 (0.00) [0]
12	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE	3/2019	9/2020 (-) [0/0]	347.78 (-) [347.78]	58.02 (0.00) [0]
13	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG	3/2019	10/2020 (-) [0/0]	394.27 (-) [394.27]	25.72 (0.00) [0]
14	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2	3/2019	2/2020 (-) [0/0]	342.55 (-) [342.55]	144.45 (0.00) [0]
15	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE	3/2019	11/2020 (-) [0/0]	421.48 (-) [421.48]	24.12 (0.00) [0]

16	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120.	12/2016	/ (-) [0/0]	200.44 (-) [200.44]	115.89 (0.00) [0]
17	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50	9/2016	/ (-) [0/0]	568.92 (-) [568.92]	260.57 (0.00) [0]
18	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5	12/2016	/ (-) [0/0]	188.78 (-) [188.78]	91.23 (0.00) [0]
19	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	12/2016	1/2017 (-) [0/0]	138.93 (155.00) [155.00]	79.91 (16.07) [0]
20	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37	4/2016	/ (-) [0/0]	245.79 (-) [245.79]	178.10 (0.00) [0]
21	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM.	4/2016	10/2016 (-) [0/0]	198.00 (-) [198.00]	184.62 (0.00) [0]
22	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH	7/2015	10/2018 (-) [0/0]	197.16 (-) [197.16]	91.25 (0.00) [0]
23	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF	3/2017	/ (-) [0/0]	1,718.59 (-) [1,718.59]	265.00 (0.00) [0]
24	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68.	8/2020	4/2022 (-) [4/2022]	301.06 (-) [301.06]	0.00 (0.00) [0]
25	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO	9/2020	5/2022 (-) [5/2022]	353.90 (-) [353.90]	4.21 (0.00) [0]
26	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	1/2017	3/2017 (-) [3/2022]	1,253.10 (-) [1,253.10]	204.77 (0.00) [60]
27	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	2/2017	4/2017 (-) [0/0]	167.28 (-) [167.28]	22.06 (0.00) [0]
28	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K	3/2018	/ (-) [0/0]	392.60 (-) [392.60]	0.00 (0.00) [0]
29	FUNDED)CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH	11/2015	/ (-) [0/0]	434.06 (-) [434.06]	172.89 (0.00) [0]
30	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017 (3/2018) [3/2021]	284.09 (284.09) [284.09]	152.19 (0.00) [0]
31	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017 (-) [0/0]	195.23 (-) [252.79]	102.51 (57.56) [0]
32	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	2/2017	4/2017 (-) [0/0]	203.36 (-) [263.31]	117.81 (59.95) [0]
33	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	194.66 (-) [252.05]	113.63 (57.39) [0]
34	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	198.22 (-) [252.05]	113.63 (53.83) [0]
35	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	3/2012	5/2012 (6/2018) [0/0]	207.03 (-) [389.45]	308.09 (182.42) [0]
36	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON	2/2017	4/2017	180.57	52.65

	EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX		(-) [2/2021]	(-) [180.57]	(0.00) [0]
37	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	12/2011	2/2012 (-) [0/0]	156.63 (276.00) [276.00]	0.00 (119.37) [0]
38	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P	11/2010	3/2011 (-) [0/0]	305.49 (-) [305.49]	131.08 (0.00) [0]
39	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI	1/2017	/ (-) [0/0]	256.66 (-) [256.66]	24.14 (0.00) [0]
40	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0	2/2017	/ (-) [4/2022]	175.06 (-) [175.06]	82.18 (0.00) [-]
41	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1	2/2017	/ (-) [4/2022]	176.12 (-) [176.12]	67.95 (0.00) [-]
42	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU	9/2011	/ (3/2020) [0/0]	1,979.00 (-) [2,036.90]	1,237.25 (57.90) [0]
	<u>ASSAM</u>				
	<u>Civil Aviation</u>				
43	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	3/2021 (3/2022) [3/2022]	1,142.00 (-) [1,232.00]	368.37 (90.00) [12]
	<u>Health And Family Welfare</u>				
44	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021 (-) [7/2022]	875.00 (-) [747.80]	331.55 (-127.20) [14]
45	LGBRIMH-TEZPUR, ASSAM	7/2012	12/2014 (-) [3/2018]	175.57 (-) [175.57]	163.37 (0.00) [0]
	<u>Petroleum</u>				
46	BS VI PROJECT AT GUWAHATI REFINERY	8/2018	2/2020 (6/2021) [6/2021]	557.00 (-) [557.00]	496.45 (0.00) [16]
47	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN	6/2016	8/2020 (-) [6/2021]	224.75 (-) [222.21]	166.48 (-2.54) [10]
48	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	6/2016	8/2019 (6/2021) [6/2021]	423.00 (-) [502.00]	422.12 (79.00) [22]
49	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (-) [6/2021]	543.91 (-) [652.10]	320.30 (108.19) [16]
50	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY	1/2019	10/2024 (-) [10/2024]	12,366.00 (-) [12,366.00]	168.82 (0.00) [0]
51	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES	1/2019	10/2024 (-) [10/2024]	10,228.00 (-) [10,228.00]	117.34 (0.00) [0]
52	PIPELINE NETWORK PROJECT GELEKI, ASSAM	7/2016	5/2020 (5/2021) [5/2021]	249.85 (303.75) [303.75]	199.31 (53.90) [12]
	<u>Railways</u>				
53	AMBARI FALAKATA TO NEW MAYNAGURI	4/2011	3/2019 (-) [3/2021]	314.00 (486.96) [800.00]	823.02 (486.00) [0]
54	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-) [3/2023]	2,232.32 (-) [2,950.00]	1,620.12 (717.68) [12]

55	DIGARU-HOJAI (102 KM)	4/2015	3/2021 (-) [5/2021]	870.96 (-) [1,873.21]	1,309.41 (1,002.25) [2]
56	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [3/2023]	385.20 (-) [1,043.00]	837.67 (657.80) [48]
	Road Transport And Highways				
57	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (-) [0/0]	268.08 (-) [390.73]	283.52 (122.65) [0]
58	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	11/2010	2/2011 (-) [0/0]	470.20 (-) [630.36]	386.98 (160.16) [0]
59	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB)	3/2020	3/2022 (-) [3/2022]	216.49 (-) [216.49]	3.35 (0.00) [0]
60	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	12/2015	6/2018 (-) [0/0]	223.30 (-) [223.30]	111.16 (0.00) [0]
61	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-) [0/0]	520.01 (-) [303.49]	174.66 (-216.52) [0]
62	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [0/0]	588.95 (-) [588.95]	420.91 (0.00) [0]
63	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [0/0]	289.99 (-) [196.24]	76.89 (-93.75) [0]
64	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (-) [0/0]	252.00 (-) [223.50]	22.91 (-28.50) [0]
65	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	6/2018 (-) [12/2021]	437.39 (-) [407.30]	21.46 (-30.09) [42]
66	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	1/2016 (-) [4/2021]	294.17 (-) [294.17]	121.82 (0.00) [63]
67	4-LANING OF HAPACHARA - TULUNGIA SECTION	3/2020	12/2022 (-) [12/2022]	220.20 (-) [220.20]	0.00 (0.00) [0]
68	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W	3/2020	12/2020 (-) [0/0]	166.94 (-) [166.94]	0.00 (0.00) [0]
69	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	4/2010 (-) [7/2019]	217.61 (-) [360.84]	489.84 (143.23) [0]
70	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM	11/2010	2/2014 (-) [0/0]	197.37 (-) [197.37]	88.86 (0.00) [0]
71	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	5/2008 (-) [6/2019]	160.00 (-) [167.98]	233.27 (7.98) [0]
72	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52	6/2016	1/2019 (-) [0/0]	829.00 (-) [829.00]	350.14 (0.00) [0]
73	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [0/0]	168.39 (-) [168.39]	134.98 (0.00) [0]
74	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE	10/2017	/ (-) [0/0]	818.00 (-) [887.68]	151.62 (69.68) [0]

75	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5	6/2015	6/2018 (-) [12/2021]	463.49 (-) [398.06]	59.71 (-65.43) [42]
76	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	3/2015	1/2016 (-) [0/0]	829.00 (-) [829.00]	415.82 (0.00) [0]
77	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (-) [12/2020]	454.89 (-) [454.89]	175.00 (0.00) [0]
78	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	2/2009 (-) [0/0]	280.00 (-) [520.00]	612.58 (240.00) [0]
79	HARANGAJO TO MAIBANG, NH-54	12/2003	7/2009 (-) [0/0]	196.00 (-) [655.17]	655.17 (459.17) [0]
80	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008 (-) [0/0]	155.04 (-) [255.23]	251.39 (100.19) [0]
81	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	4/2009 (-) [0/0]	199.81 (-) [340.14]	325.28 (140.33) [0]
82	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008 (-) [0/0]	167.64 (-) [435.78]	427.96 (268.14) [0]
83	NALBARI T BIJNI (AS-7)	12/2003	4/2008 (-) [2/2021]	208.00 (-) [230.00]	370.56 (22.00) [0]
84	NALBARI TO BIJNI (AS-6)	12/2003	6/2008 (-) [9/2019]	225.00 (-) [225.00]	390.72 (0.00) [0]
85	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST	3/2017	/ (-) [0/0]	1,049.51 (-) [273.40]	98.01 (-776.11) [0]
86	SONAPUR TO GUWAHTI (AS-3)	12/2003	3/2008 (-) [8/2020]	245.00 (-) [174.34]	240.36 (-70.66) [0]
87	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN	9/2018	9/2021 (-) [9/2021]	160.00 (-) [160.00]	101.70 (0.00) [0]
88	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800	8/2020	4/2022 (-) [4/2022]	208.84 (-) [208.84]	0.00 (0.00) [0]
89	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923	8/2020	3/2022 (-) [3/2022]	278.46 (-) [278.46]	12.06 (0.00) [0]
	<u>MANIPUR</u>				
	<u>Power</u>				
90	LOKTAK D/S HEP(NHPC)	12/1999	6/2006 (-) [0/0]	578.62 (-) [578.62]	0.00 (0.00) [0]
	<u>Railways</u>				
91	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (-) [12/2023]	4,454.17 (-) [12,264.15]	10,994.55 (7,809.98) [153]
	<u>Road Transport And Highways</u>				
92	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A)	3/2020	6/2022 (-) [6/2022]	292.24 (-) [292.24]	1.74 (0.00) [0]
93	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B)	6/2020	8/2022 (-) [8/2022]	365.53 (-) [365.53]	3.35 (0.00) [0]

94	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A)	3/2020	6/2022 (-) [6/2022]	167.95 (-) [167.95]	1.12 (0.00) [0]
95	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B)	7/2020	8/2022 (-) [8/2022]	177.76 (-) [177.76]	0.64 (0.00) [0]
96	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO	8/2020	4/2022 (-) [4/2022]	268.98 (-) [268.98]	0.00 (0.00) [0]
97	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI	8/2020	4/2022 (-) [4/2022]	228.97 (-) [228.97]	0.00 (0.00) [0]
98	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI	8/2020	4/2022 (-) [4/2022]	379.39 (-) [379.39]	0.00 (0.00) [0]
99	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137	3/2019	7/2022 (-) [7/2022]	471.00 (-) [471.00]	0.00 (0.00) [0]
100	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260.	10/2016	11/2020 (-) [11/2020]	235.31 (-) [235.31]	184.33 (0.00) [0]
101	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	8/2017	10/2018 (-) [10/2021]	517.57 (-) [457.77]	137.04 (-59.80) [36]
	<u>MEGHALAYA</u>				
	<u>Culture Development</u>				
102	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGHALAYA UNDER NLCPR	4/2014	9/2017 (-) [3/2021]	151.33 (-) [151.33]	148.33 (0.00) [0]
	<u>Health And Family Welfare</u>				
103	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (-) [12/2021]	363.99 (-) [363.99]	239.89 (0.00) [43]
	<u>Human Resource Development</u>				
104	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	9/2013	9/2014 (-) [0/0]	484.32 (-) [626.26]	0.00 (141.94) [0]
	<u>Railways</u>				
105	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [0/0]	906.46 (1,202.33) [4,083.02]	264.33 (3,176.56) [0]
	<u>Road Transport And Highways</u>				
106	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	3/2019	5/2019 (-) [0/0]	306.28 (-) [306.28]	78.34 (0.00) [0]
107	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	12/2015	5/2018 (-) [0/0]	479.20 (-) [479.20]	712.89 (0.00) [0]
108	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	/ (-) [9/2021]	553.51 (-) [553.51]	75.51 (0.00) [-]
	<u>MIZORAM</u>				
	<u>Railways</u>				
109	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (-) [3/2023]	2,393.47 (5,021.45) [5,521.45]	3,954.28 (3,127.98) [108]
	<u>Road Transport And Highways</u>				
110	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (-) [6/2021]	195.04 (-) [377.99]	331.49 (182.95) [128]
111	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM	8/2010	9/2014	186.96	298.52

	38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD		(-) [6/2021]	(-) [322.24]	(135.28) [81]
112	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (-) [6/2021]	193.69 (-) [327.92]	301.46 (134.23) [128]
113	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54	9/2020	10/2022 (-) [10/2022]	275.02 (-) [275.02]	14.15 (0.00) [0]
114	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I)	3/2020	7/2022 (-) [7/2022]	206.88 (-) [206.88]	9.33 (0.00) [0]
115	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II)	3/2020	7/2022 (-) [7/2022]	216.49 (-) [216.49]	28.93 (0.00) [0]
116	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III)	3/2020	7/2022 (-) [7/2022]	292.24 (-) [292.24]	29.00 (0.00) [0]
117	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV)	3/2020	7/2022 (-) [7/2022]	281.78 (-) [281.78]	38.40 (0.00) [0]
118	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2023]	519.09 (-) [519.09]	56.58 (0.00) [43]
119	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [7/2023]	640.07 (-) [640.07]	3.25 (0.00) [46]
120	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [6/2023]	642.96 (-) [642.96]	82.00 (0.00) [45]
121	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2024]	404.29 (-) [404.29]	17.77 (0.00) [55]
122	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2023]	428.11 (-) [428.11]	48.03 (0.00) [48]
123	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [6/2023]	518.53 (-) [518.53]	108.99 (0.00) [45]
124	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2023]	537.82 (-) [537.82]	100.74 (0.00) [43]
125	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2023]	473.18 (-) [473.18]	81.00 (0.00) [43]
126	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (-) [12/2020]	624.41 (-) [992.67]	890.74 (368.26) [0]
	<u>NAGALAND</u>				
	<u>Railways</u>				
127	DIMAPUR-TIZIT NL	4/2013	3/2020 (-) [0/0]	4,274.00 (-) [4,274.00]	0.00 (0.00) [0]
128	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015 (-) [12/2024]	2,326.52 (-) [6,911.00]	1,204.64 (4,584.48) [117]
	<u>Road Transport And Highways</u>				
129	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018 (-) [5/2022]	239.30 (-) [239.30]	102.01 (0.00) [44]
130	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM	3/2018	9/2018 (-)	285.68 (-)	77.91 (0.00)

	EXISTING KM 52.370 TO		[9/2022]	[285.68]	[48]
131	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	3/2018	9/2018 (-) [0/0]	282.98 (-) [192.60]	127.31 (-90.38) [0]
132	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018 (-) [9/2020]	387.00 (-) [387.00]	283.11 (0.00) [0]
133	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	9/2018 (-) [11/2022]	500.09 (336.49) [336.49]	79.51 (-163.60) [50]
134	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I)	3/2020	6/2022 (-) [6/2022]	320.97 (-) [320.97]	18.73 (0.00) [0]
135	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II)	3/2020	6/2022 (-) [6/2022]	355.79 (-) [355.79]	31.76 (0.00) [0]
136	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III)	3/2020	6/2022 (-) [6/2022]	361.53 (-) [361.53]	13.17 (0.00) [0]
137	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV)	3/2020	12/2021 (-) [12/2021]	330.78 (-) [330.78]	23.74 (0.00) [0]
138	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V)	4/2020	12/2021 (-) [12/2021]	330.80 (-) [330.80]	11.57 (0.00) [0]
139	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I)	3/2020	6/2022 (-) [6/2022]	278.95 (-) [278.95]	56.76 (0.00) [0]
140	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN	3/2017	11/2020 (5/2021) [11/2020]	217.35 (-) [217.35]	97.62 (0.00) [0]
141	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T	9/2020	4/2022 (-) [4/2022]	257.15 (-) [257.15]	17.77 (0.00) [0]
142	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES	8/2020	4/2022 (-) [4/2022]	202.36 (-) [202.36]	0.00 (0.00) [0]
143	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D	8/2020	4/2022 (-) [4/2022]	232.29 (-) [232.29]	0.00 (0.00) [0]
144	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D	9/2020	10/2022 (-) [10/2022]	277.44 (-) [277.44]	0.00 (0.00) [0]
145	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG	8/2020	10/2022 (-) [10/2022]	159.85 (-) [159.85]	0.00 (0.00) [0]
146	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683	2/2017	4/2017 (-) [0/0]	507.68 (-) [507.68]	129.13 (0.00) [0]
147	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [7/2022]	339.57 (-) [339.57]	141.46 (0.00) [46]
148	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	3/2018	9/2018 (-) [12/2021]	315.03 (-) [315.03]	88.52 (0.00) [39]
149	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	9/2018 (-) [12/2021]	240.64 (-) [240.64]	102.51 (0.00) [39]
150	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [11/2021]	215.12 (-) [215.12]	100.90 (0.00) [38]

151	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	9/2018 (-) [12/2021]	215.79 (-) [215.79]	67.30 (0.00) [39]
152	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [10/2022]	272.89 (-) [272.89]	51.17 (0.00) [49]
153	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	3/2018	9/2018 (-) [11/2022]	323.98 (-) [323.98]	42.54 (0.00) [50]
154	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0	3/2018	9/2018 (-) [0/0]	251.97 (-) [251.97]	138.60 (0.00) [0]
155	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (-) [0/0]	237.72 (-) [237.72]	109.96 (0.00) [0]
156	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	8/2016 (-) [5/2021]	373.07 (-) [387.00]	245.80 (13.93) [57]
157	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2016 (-) [5/2021]	396.52 (-) [339.55]	252.49 (-56.97) [57]
158	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	3/2016	8/2016 (-) [5/2021]	429.52 (-) [340.00]	193.99 (-89.52) [57]
159	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M	11/2016	9/2019 (11/2020) [0/0]	336.25 (369.96) [336.25]	322.13 (0.00) [0]
160	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (9/2021) [12/2020]	167.62 (-) [167.62]	104.39 (0.00) [0]
161	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (9/2021) [12/2020]	172.63 (-) [172.63]	129.65 (0.00) [0]
162	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM	9/2020	4/2022 (-) [4/2022]	315.63 (-) [315.63]	0.00 (0.00) [0]
163	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA	12/2010	2/2011 (-) [0/0]	1,296.00 (-) [1,296.00]	0.00 (0.00) [0]
164	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH-	3/2019	12/2022 (-) [12/2022]	237.51 (-) [237.51]	60.04 (0.00) [0]
	SIKKIM				
	Railways				
165	SEVOK RANGPO, NEFR	4/2008	12/2015 (-) [0/0]	1,339.48 (-) [8,600.00]	619.18 (7,260.52) [0]
	Road Transport And Highways				
166	CONSTRUCTION & UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	8/2020	4/2023 (-) [4/2023]	311.00 (-) [311.00]	0.00 (0.00) [0]
167	CONSTRUCTION & UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	7/2020	4/2023 (-) [4/2023]	345.38 (-) [345.38]	0.00 (0.00) [0]
168	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	1/2013	2/2013 (6/2021) [6/2021]	182.28 (369.64) [369.64]	274.07 (187.36) [100]
169	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	4/2013	8/2013 (6/2021) [6/2021]	151.59 (370.01) [370.01]	281.74 (218.42) [94]
170	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI	4/2013	8/2013	166.27	243.59

	ROAD IN SOUTH SIKKIM.		(6/2021) [6/2021]	(359.92) [359.92]	(193.65) [94]
171	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	3/2017	/ (-) [0/0]	375.80 (-) [375.80]	52.88 (0.00) [0]
172	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	11/2017	11/2017 (-) [0/0]	290.05 (-) [290.05]	97.21 (0.00) [0]
173	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA	4/2017	11/2017 (-) [0/0]	318.42 (-) [318.42]	66.63 (0.00) [0]
174	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	3/2018	6/2018 (-) [0/0]	264.84 (-) [264.84]	0.00 (0.00) [0]
175	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N	3/2019	4/2022 (-) [4/2022]	402.94 (-) [402.94]	0.00 (0.00) [0]
176	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600	8/2020	4/2023 (-) [4/2023]	295.97 (-) [295.97]	0.00 (0.00) [0]
177	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00	3/2020	6/2022 (-) [6/2022]	242.97 (-) [242.97]	0.00 (0.00) [0]
178	RHENOK-RORATHANG-PAKYONG ON NH 717A	4/2017	10/2017 (-) [0/0]	388.00 (-) [447.37]	261.20 (59.37) [0]
	<u>TRIPURA</u>				
	<u>Civil Aviation</u>				
179	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	9/2015	6/2019 (12/2020) [6/2021]	438.28 (-) [402.00]	366.61 (-36.28) [24]
	<u>Railways</u>				
180	AGARTALA-AKHAURA NL	4/2012	3/2020 (-) [3/2022]	569.63 (-) [742.00]	200.28 (172.37) [24]
	<u>Road Transport And Highways</u>				
181	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S	10/2014	3/2018 (-) [0/0]	369.00 (-) [369.00]	322.69 (0.00) [0]
182	2-LANING FROM MANU-SIMLUNG (PKG I)	3/2020	1/2022 (-) [1/2022]	247.76 (-) [247.76]	2.60 (0.00) [0]
183	2-LANING FROM MANU-SIMLUNG (PKG III)	6/2020	1/2022 (-) [1/2022]	347.36 (-) [347.36]	0.00 (0.00) [0]
184	REHABILITATION & UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE SE	3/2020	7/2022 (-) [7/2022]	154.51 (-) [154.51]	0.00 (0.00) [0]
185	REHABILITATION & UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION	6/2020	1/2022 (-) [1/2022]	277.50 (-) [277.50]	0.00 (0.00) [0]
186	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID	3/2020	7/2022 (-) [7/2022]	178.43 (-) [178.43]	0.00 (0.00) [0]
187	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K	1/2017	12/2022 (-) [12/2022]	197.67 (-) [197.67]	5.75 (0.00) [0]
188	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C	10/2016	8/2020 (-) [7/2021]	171.90 (-) [171.90]	123.81 (0.00) [11]
	<u>Rural Development</u>				

189	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	3/2007	12/2015 (-) [10/2021]	149.73 (173.00) [155.66]	144.95 (5.93) [70]
190	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016 (-) [10/2021]	202.61 (227.00) [207.12]	190.22 (4.51) [58]
191	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	12/2016 (-) [12/2021]	175.49 (206.71) [175.49]	124.87 (0.00) [60]
	Total			1,13,904.42 (38,272.58) [1,64,445.17]	69,109.10 (50,540.75)

Details of Central Sector Projects Costing Rs.150 crore and above (as on					30.04.2021)
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	<u>A & N ISLANDS</u>				
	<u>Civil Aviation</u>				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	9/2018 (9/2020) [6/2021]	417.23 (707.73) [707.73]	379.95 (290.50) [33]
	<u>Road Transport And Highways</u>				
2	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N	3/2017	12/2017 (-) [0/0]	409.85 (-) [409.85]	21.11 (0.00) [0]
3	AJANTHA TO BULDHANA	2/2017	7/2019 (-) [0/0]	401.00 (401.00) [401.00]	143.81 (0.00) [0]
4	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C	3/2015	4/2017 (-) [0/0]	277.17 (-) [277.17]	159.49 (0.00) [0]
5	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (	3/2015	10/2018 (-) [0/0]	262.97 (-) [262.97]	0.00 (0.00) [0]
6	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	11/2017	11/2019 (-) [0/0]	257.34 (-) [238.00]	41.09 (-19.34) [0]
7	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM	2/2018	10/2018 (-) [0/0]	391.00 (-) [391.00]	22.17 (0.00) [0]
8	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O	3/2018	10/2018 (-) [0/0]	234.27 (-) [234.27]	11.03 (0.00) [0]
9	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00	11/2017	11/2019 (-) [0/0]	237.80 (-) [238.00]	7.48 (0.20) [0]
	<u>ANDHRA PRADESH</u>				
	<u>Civil Aviation</u>				
10	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT	4/2020	3/2023 (-) [3/2023]	611.80 (-) [611.80]	21.25 (0.00) [0]
11	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT	8/2017	2/2020 (6/2021) [12/2021]	177.10 (-) [177.10]	86.01 (0.00) [22]
	<u>Health And Family Welfare</u>				
12	HOSPITAL AND TEACHING- AIIMS GUNTUR	3/2018	/ (-) [6/2021]	601.02 (-) [601.02]	400.25 (0.00) [-]
13	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS- MNAGLAGIRI GUNTUR, ANDHRA PRADESH	8/2017	3/2019 (-) [3/2021]	272.19 (-) [272.54]	272.54 (0.35) [0]
	<u>Human Resource Development</u>				
14	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P.	2/2019	9/2020 (-)	186.00 (199.00)	130.63 (19.00)

			[0/0]	[205.00]	[0]
15	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRICT	9/2019	9/2022 (-) [1/2023]	588.72 (-) [588.72]	14.80 (0.00) [4]
16	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE	2/2019	6/2020 (-) [0/0]	655.34 (-) [655.34]	49.89 (0.00) [0]
	<u>Petroleum</u>				
17	220 KV GRID SUPPLY	10/2020	3/2021 (-) [0/0]	303.40 (-) [303.40]	199.17 (0.00) [0]
18	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH	8/2018	4/2021 (12/2021) [12/2021]	466.00 (-) [466.00]	256.49 (0.00) [8]
19	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP	8/2017	4/2021 (3/2021) [3/2021]	384.58 (-) [384.58]	248.75 (0.00) [0]
20	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT	7/2017	2/2021 (-) [3/2023]	580.20 (-) [580.20]	155.84 (0.00) [25]
21	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	3/2016	6/2020 (6/2022) [6/2022]	34,012.00 (-) [25,090.00]	11,254.33 (-8,922.00) [24]
22	LPG BP PROJECT CHITTOOR	7/2019	7/2022 (-) [7/2022]	167.00 (-) [167.00]	8.89 (0.00) [0]
23	REVAMPING OF FACILITIES AT VIZAG TERMINAL	4/2018	4/2022 (-) [2/2023]	355.00 (-) [355.00]	106.53 (0.00) [10]
24	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP	10/2018	10/2021 (3/2022) [3/2022]	316.20 (-) [316.20]	98.14 (0.00) [5]
25	RUF PITCH LOADING GANTRY	10/2020	11/2022 (-) [11/2022]	332.61 (-) [332.61]	0.01 (0.00) [0]
26	SULPHUR FORMING UNIT IN SRU	10/2020	8/2021 (-) [8/2021]	210.94 (-) [210.94]	117.03 (0.00) [0]
27	SWRO II WITH LLPH FACILITIES	9/2019	7/2020 (-) [7/2021]	196.26 (-) [196.26]	92.38 (0.00) [12]
28	VISAKH REFINERY MODERNISATION PROJECT	7/2016	7/2020 (7/2022) [7/2022]	20,928.00 (26,264.00) [26,264.00]	14,820.38 (5,336.00) [24]
	<u>Railways</u>				
29	CUMBUM-PRODDATUR	4/2013	/ (-) [0/0]	829.00 (-) [829.00]	0.94 (0.00) [0]
30	DUVVADA-VIJAYAWADA	4/2015	/ (-) [0/0]	3,873.07 (-) [3,873.07]	0.38 (0.00) [0]
31	GUDUR-DURGARA JAPATNAM	4/2011	/ (-) [0/0]	761.37 (-) [761.37]	0.52 (0.00) [0]
32	GUNTUR-GUNTAKAL	4/2016	3/2022 (-) [3/2024]	3,631.00 (-) [3,887.48]	1,144.64 (256.48) [24]
33	KOTLPALLI-NARASAPUR (NL) (SCR)	12/2001	3/2009 (-) [3/2024]	1,045.20 (-) [2,120.16]	883.52 (1,074.96) [180]
34	KOTTAVALSA - KORAPUT DOUBLING	4/2015	3/2022	2,499.71	671.08

			(3/2024) [3/2024]	(-) [2,499.71]	(0.00) [24]
35	MULTI MODAL LOGISTICS PARK AT KAKINADA	8/2016	3/2019 (-) [0/0]	234.50 (-) [235.00]	14.14 (0.50) [0]
36	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM	1/2013	3/2018 (-) [3/2021]	387.70 (-) [487.13]	434.63 (99.43) [0]
37	NADIKUDE-SRI KALAHASTI	4/2011	3/2021 (-) [3/2024]	2,288.70 (-) [2,643.25]	1,231.85 (354.55) [36]
38	NANDYAL-YERRAGUNTLA(NL),SCR	3/1996	2/2009 (-) [0/0]	164.36 (-) [1,050.00]	999.64 (885.64) [0]
39	VIJAYAWADA-GUDUR	4/2015	12/2023 (-) [12/2023]	3,246.26 (-) [3,548.68]	2,224.17 (302.42) [0]
40	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	3/2012	3/2020 (-) [3/2022]	1,503.71 (-) [3,377.00]	2,683.67 (1,873.29) [24]
Road Transport And Highways					
41	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM	12/2017	/ (-) [0/0]	328.67 (-) [328.67]	234.49 (0.00) [0]
42	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0	11/2019	2/2021 (-) [0/0]	1,226.88 (-) [1,226.88]	0.00 (0.00) [0]
43	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881)	11/2019	2/2021 (-) [0/0]	1,601.10 (-) [1,601.10]	0.00 (0.00) [0]
44	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O	12/2017	/ (-) [0/0]	357.00 (-) [357.00]	0.00 (0.00) [0]
45	CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415	3/2018	/ (-) [0/0]	557.30 (-) [557.30]	351.02 (0.00) [0]
46	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216	1/2017	9/2017 (-) [5/2021]	263.45 (-) [263.45]	97.45 (0.00) [44]
47	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V	2/2017	11/2017 (4/2021) [4/2021]	429.43 (-) [429.43]	256.15 (0.00) [41]
48	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1	3/2018	/ (-) [3/2022]	314.43 (-) [314.43]	85.61 (0.00) [-]
49	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD	8/2016	1/2017 (-) [12/2020]	350.61 (-) [350.61]	323.06 (0.00) [0]
50	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C	10/2015	11/2015 (-) [0/0]	333.21 (-) [353.89]	256.11 (20.68) [0]
51	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C	7/2015	12/2015 (-) [0/0]	333.21 (333.21) [333.21]	256.11 (0.00) [0]
52	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0)	7/2015	12/2015 (-) [0/0]	333.21 (-) [333.21]	256.11 (0.00) [0]
53	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12	10/2015	12/2015 (-) [0/0]	333.21 (-) [355.89]	315.57 (22.68) [0]
54	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-	3/2018	3/2021	1,532.62	761.73

	KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)		(10/2021) [4/2021]	(-) [2,499.00]	(966.38) [1]
55	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHILIPATNAM (KM 0.000 TO 63.800)	1/2016	11/2018 (-) [0/0]	1,134.97 (-) [1,134.97]	1,634.05 (0.00) [0]
56	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH	1/2017	1/2018 (-) [0/0]	576.48 (-) [576.48]	288.92 (0.00) [0]
57	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT	1/2016	8/2016 (-) [7/2021]	348.95 (-) [348.95]	200.57 (0.00) [59]
58	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S	7/2014	2/2015 (-) [0/0]	251.55 (-) [251.55]	7.74 (0.00) [0]
59	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21	1/2016	5/2016 (-) [0/0]	386.09 (-) [386.09]	199.35 (0.00) [0]
60	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69	11/2016	5/2017 (7/2021) [7/2021]	290.15 (-) [290.15]	73.11 (0.00) [50]
61	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T	1/2014	11/2014 (-) [0/0]	195.45 (-) [195.45]	0.00 (0.00) [0]
62	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS	3/2018	/ (-) [2/2021]	565.09 (-) [565.09]	601.35 (0.00) [0]
63	REHABILITATION AND UPGRADATION OF KARNATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O	3/2016	5/2016 (-) [4/2021]	995.09 (995.00) [995.09]	476.77 (0.00) [59]
64	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216	3/2016	9/2016 (-) [0/0]	444.84 (-) [444.84]	304.42 (0.00) [0]
65	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2	11/2016	8/2017 (-) [0/0]	376.25 (-) [376.25]	264.97 (0.00) [0]
66	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (	3/2018	7/2018 (-) [0/0]	297.12 (294.00) [294.12]	373.98 (-3.00) [0]
67	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG	3/2018	8/2018 (-) [2/2021]	289.67 (290.00) [289.67]	177.78 (0.00) [0]
68	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA	3/2018	11/2018 (-) [1/2021]	504.19 (504.00) [504.19]	427.08 (0.00) [0]
69	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES	3/2015	10/2015 (-) [3/2021]	271.45 (-) [271.45]	225.81 (0.00) [0]
70	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD	1/2017	8/2017 (-) [8/2019]	319.28 (-) [319.28]	214.00 (0.00) [0]
71	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU	3/2018	8/2018 (-) [0/0]	244.95 (245.00) [244.95]	136.22 (0.00) [0]
72	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU	9/2016	2/2017 (6/2021) [6/2021]	372.68 (-) [372.68]	185.04 (0.00) [52]
73	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3	3/2018	8/2018 (-) [3/2021]	228.32 (-) [228.32]	105.72 (0.00) [0]
74	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM	1/2018	8/2018 (5/2021)	418.03 (-)	194.62 (0.00)

	420.800(P		[5/2021]	[418.03]	[33]
75	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO	11/2016	1/2018 (-) [0/0]	378.24 (-) [378.24]	315.42 (0.00) [0]
76	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM	2/2018	/	1,959.00	1,211.72
			(-) [10/2021]	(-) [1,959.00]	(0.00) [-]
77	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105	9/2018	1/2020 (-) [0/0]	597.67 (-) [597.67]	0.00 (0.00) [0]
78	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN	9/2018	2/2019 (-) [0/0]	617.41 (-) [617.41]	0.00 (0.00) [0]
79	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN	12/2017	/	1,323.15	785.33
			(-) [7/2021]	(-) [1,323.15]	(0.00) [-]
80	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG	3/2018	/	1,550.98	1,401.00
			(-) [9/2021]	(-) [1,550.98]	(0.00) [-]
81	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	11/2011	5/2014 (-) [0/0]	1,535.00 (-) [1,535.00]	3,278.00 (0.00) [0]
82	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	3/2017	3/2020 (-) [0/0]	1,041.62 (-) [1,187.10]	951.13 (145.48) [0]
83	TIRUPATI - TIRUTHANI - CHENNAI	4/2011	10/2013 (-) [0/0]	571.00 (-) [571.00]	582.53 (0.00) [0]
84	VIJAYAWADA-GUNDUGOLANU SECTION	9/2014	2/2017 (-) [0/0]	1,684.00 (-) [1,684.00]	54.13 (0.00) [0]
	<u>Steel</u>				
85	COKE OVEN BATTERY-5	12/2011	12/2017 (12/2021) [12/2021]	2,858.00 (-) [2,558.00]	1,838.96 (-300.00) [48]
	<u>Water Resources</u>				
86	POLAVARAM IRRIGATION PROJECT	2/2009	3/2020 (11/2021) [4/2022]	10,151.04 (55,548.87) [55,548.87]	17,325.20 (45,397.83) [25]
	<u>ARUNACHAL PRADESH</u>				
	<u>Power</u>				
87	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009 (2/2021) [0/0]	2,496.90 (7,927.34) [7,927.34]	8,225.88 (5,430.44) [0]
88	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (8/2023) [8/2023]	6,285.33 (19,992.43) [19,992.43]	13,732.39 (13,707.10) [155]
	<u>Road Transport And Highways</u>				
89	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN	3/2015	/	172.75	134.38
			(-) [0/0]	(-) [172.75]	(0.00) [0]
90	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	3/2015	6/2018 (-) [0/0]	394.00 (-) [394.00]	400.56 (0.00) [0]
91	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX	10/2015	/	210.50	145.07
			(1/2016) [1/2019]	(210.50) [210.50]	(0.00) [0]
92	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST	11/2016	/	243.89	145.31
			(-) [9/2020]	(-) [243.89]	(0.00) [0]
93	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN	3/2019	2/2020	403.68	40.08

	SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1)		(-) [0/0]	(-) [403.68]	(0.00) [0]
94	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE	3/2019	11/2020 (-) [0/0]	543.05 (-) [543.05]	86.24 (0.00) [0]
95	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE	3/2019	11/2020 (-) [0/0]	450.65 (-) [450.65]	6.51 (0.00) [0]
96	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE	3/2019	10/2020 (-) [0/0]	486.70 (-) [486.70]	54.10 (0.00) [0]
97	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE	3/2019	2/2020 (-) [0/0]	560.39 (-) [560.39]	118.45 (0.00) [0]
98	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE	3/2019	9/2020 (-) [0/0]	347.78 (-) [347.78]	58.02 (0.00) [0]
99	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG	3/2019	10/2020 (-) [0/0]	394.27 (-) [394.27]	25.72 (0.00) [0]
100	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2	3/2019	2/2020 (-) [0/0]	342.55 (-) [342.55]	144.45 (0.00) [0]
101	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE	3/2019	11/2020 (-) [0/0]	421.48 (-) [421.48]	24.12 (0.00) [0]
102	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120.	12/2016	/ (-) [0/0]	200.44 (-) [200.44]	115.89 (0.00) [0]
103	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50	9/2016	/ (-) [0/0]	568.92 (-) [568.92]	260.57 (0.00) [0]
104	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5	12/2016	/ (-) [0/0]	188.78 (-) [188.78]	91.23 (0.00) [0]
105	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	12/2016	1/2017 (-) [0/0]	138.93 (155.00) [155.00]	79.91 (16.07) [0]
106	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37	4/2016	/ (-) [0/0]	245.79 (-) [245.79]	178.10 (0.00) [0]
107	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM.	4/2016	10/2016 (-) [0/0]	198.00 (-) [198.00]	184.62 (0.00) [0]
108	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH	7/2015	10/2018 (-) [0/0]	197.16 (-) [197.16]	91.25 (0.00) [0]
109	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF	3/2017	/ (-) [0/0]	1,718.59 (-) [1,718.59]	265.00 (0.00) [0]
110	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68.	8/2020	4/2022 (-) [4/2022]	301.06 (-) [301.06]	0.00 (0.00) [0]
111	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO	9/2020	5/2022 (-) [5/2022]	353.90 (-) [353.90]	4.21 (0.00) [0]
112	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	1/2017	3/2017 (-) [3/2022]	1,253.10 (-) [1,253.10]	204.77 (0.00) [60]
113	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON	2/2017	4/2017 (-)	167.28 (-)	22.06 (0.00)

	EPC BASIS FROM EXI		[0/0]	[167.28]	[0]
114	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K	3/2018	/	392.60	0.00
			(-)	(-)	(0.00)
			[0/0]	[392.60]	[0]
115	FUNDED)CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH	11/2015	/	434.06	172.89
			(-)	(-)	(0.00)
			[0/0]	[434.06]	[0]
116	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017	284.09	152.19
			(3/2018)	(284.09)	(0.00)
			[3/2021]	[284.09]	[0]
117	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017	195.23	102.51
			(-)	(-)	(57.56)
			[0/0]	[252.79]	[0]
118	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	2/2017	4/2017	203.36	117.81
			(-)	(-)	(59.95)
			[0/0]	[263.31]	[0]
119	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017	194.66	113.63
			(-)	(-)	(57.39)
			[0/0]	[252.05]	[0]
120	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017	198.22	113.63
			(-)	(-)	(53.83)
			[0/0]	[252.05]	[0]
121	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	3/2012	5/2012	207.03	308.09
			(6/2018)	(-)	(182.42)
			[0/0]	[389.45]	[0]
122	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	2/2017	4/2017	180.57	52.65
			(-)	(-)	(0.00)
			[2/2021]	[180.57]	[0]
123	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	12/2011	2/2012	156.63	0.00
			(-)	(276.00)	(119.37)
			[0/0]	[276.00]	[0]
124	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P	11/2010	3/2011	305.49	131.08
			(-)	(-)	(0.00)
			[0/0]	[305.49]	[0]
125	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI	1/2017	/	256.66	24.14
			(-)	(-)	(0.00)
			[0/0]	[256.66]	[0]
126	TWO-LANING OF JORAM - KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0	2/2017	/	175.06	82.18
			(-)	(-)	(0.00)
			[4/2022]	[175.06]	[-]
127	TWO-LANING OF JORAM - KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1	2/2017	/	176.12	67.95
			(-)	(-)	(0.00)
			[4/2022]	[176.12]	[-]
128	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU	9/2011	/	1,979.00	1,237.25
			(3/2020)	(-)	(57.90)
			[0/0]	[2,036.90]	[0]
	ASSAM				
	Civil Aviation				
129	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	3/2021	1,142.00	368.37
			(3/2022)	(-)	(90.00)
			[3/2022]	[1,232.00]	[12]
	Health And Family Welfare				
130	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021	875.00	331.55
			(-)	(-)	(-127.20)
			[7/2022]	[747.80]	[14]
131	LGBRIMH-TEZPUR, ASSAM	7/2012	12/2014	175.57	163.37
			(-)	(-)	(0.00)
			[3/2018]	[175.57]	[0]
	Petroleum				
132	BS VI PROJECT AT GUWAHATI REFINERY	8/2018	2/2020	557.00	496.45
			(6/2021)	(-)	(0.00)

			[6/2021]	[557.00]	[16]
133	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN	6/2016	8/2020 (-) [6/2021]	224.75 (-) [222.21]	166.48 (-2.54) [10]
134	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR), CACHAR, ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	6/2016	8/2019 (6/2021) [6/2021]	423.00 (-) [502.00]	422.12 (79.00) [22]
135	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (-) [6/2021]	543.91 (-) [652.10]	320.30 (108.19) [16]
136	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY	1/2019	10/2024 (-) [10/2024]	12,366.00 (-) [12,366.00]	168.82 (0.00) [0]
137	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES	1/2019	10/2024 (-) [10/2024]	10,228.00 (-) [10,228.00]	117.34 (0.00) [0]
138	PIPELINE NETWORK PROJECT GELEKI, ASSAM	7/2016	5/2020 (5/2021) [5/2021]	249.85 (303.75) [303.75]	199.31 (53.90) [12]
	<u>Railways</u>				
139	AMBARI FALAKATA TO NEW MAYNAGURI	4/2011	3/2019 (-) [3/2021]	314.00 (486.96) [800.00]	823.02 (486.00) [0]
140	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-) [3/2023]	2,232.32 (-) [2,950.00]	1,620.12 (717.68) [12]
141	DIGARU-HOJAI (102 KM)	4/2015	3/2021 (-) [5/2021]	870.96 (-) [1,873.21]	1,309.41 (1,002.25) [2]
142	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [3/2023]	385.20 (-) [1,043.00]	837.67 (657.80) [48]
	<u>Road Transport And Highways</u>				
143	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (-) [0/0]	268.08 (-) [390.73]	283.52 (122.65) [0]
144	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	11/2010	2/2011 (-) [0/0]	470.20 (-) [630.36]	386.98 (160.16) [0]
145	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB)	3/2020	3/2022 (-) [3/2022]	216.49 (-) [216.49]	3.35 (0.00) [0]
146	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	12/2015	6/2018 (-) [0/0]	223.30 (-) [223.30]	111.16 (0.00) [0]
147	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-) [0/0]	520.01 (-) [303.49]	174.66 (-216.52) [0]
148	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [0/0]	588.95 (-) [588.95]	420.91 (0.00) [0]
149	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [0/0]	289.99 (-) [196.24]	76.89 (-93.75) [0]
150	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (-) [0/0]	252.00 (-) [223.50]	22.91 (-28.50) [0]
151	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	6/2018 (-) [12/2021]	437.39 (-) [407.30]	21.46 (-30.09) [42]
152	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END	1/2016	1/2016	294.17	121.82

	OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O		(-) [4/2021]	(-) [294.17]	(0.00) [63]
153	4-LANING OF HAPACHARA - TULUNGIA SECTION	3/2020	12/2022 (-) [12/2022]	220.20 (-) [220.20]	0.00 (0.00) [0]
154	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W	3/2020	12/2020 (-) [0/0]	166.94 (-) [166.94]	0.00 (0.00) [0]
155	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	4/2010 (-) [7/2019]	217.61 (-) [360.84]	489.84 (143.23) [0]
156	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM	11/2010	2/2014 (-) [0/0]	197.37 (-) [197.37]	88.86 (0.00) [0]
157	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	5/2008 (-) [6/2019]	160.00 (-) [167.98]	233.27 (7.98) [0]
158	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52	6/2016	1/2019 (-) [0/0]	829.00 (-) [829.00]	350.14 (0.00) [0]
159	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [0/0]	168.39 (-) [168.39]	134.98 (0.00) [0]
160	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE	10/2017	/ (-) [0/0]	818.00 (-) [887.68]	151.62 (69.68) [0]
161	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5	6/2015	6/2018 (-) [12/2021]	463.49 (-) [398.06]	59.71 (-65.43) [42]
162	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	3/2015	1/2016 (-) [0/0]	829.00 (-) [829.00]	415.82 (0.00) [0]
163	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (-) [12/2020]	454.89 (-) [454.89]	175.00 (0.00) [0]
164	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	2/2009 (-) [0/0]	280.00 (-) [520.00]	612.58 (240.00) [0]
165	HARANGAJO TO MAIBANG, NH-54	12/2003	7/2009 (-) [0/0]	196.00 (-) [655.17]	655.17 (459.17) [0]
166	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008 (-) [0/0]	155.04 (-) [255.23]	251.39 (100.19) [0]
167	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	4/2009 (-) [0/0]	199.81 (-) [340.14]	325.28 (140.33) [0]
168	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008 (-) [0/0]	167.64 (-) [435.78]	427.96 (268.14) [0]
169	NALBARI T BIJNI (AS-7)	12/2003	4/2008 (-) [2/2021]	208.00 (-) [230.00]	370.56 (22.00) [0]
170	NALBARI TO BIJNI (AS-6)	12/2003	6/2008 (-) [9/2019]	225.00 (-) [225.00]	390.72 (0.00) [0]
171	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST	3/2017	/ (-) [0/0]	1,049.51 (-) [273.40]	98.01 (-776.11) [0]
172	SONAPUR TO GUWAHTI (AS-3)	12/2003	3/2008 (-)	245.00 (-)	240.36 (-70.66)

			[8/2020]	[174.34]	[0]
173	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN	9/2018	9/2021 (-) [9/2021]	160.00 (-) [160.00]	101.70 (0.00) [0]
174	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800	8/2020	4/2022 (-) [4/2022]	208.84 (-) [208.84]	0.00 (0.00) [0]
175	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923	8/2020	3/2022 (-) [3/2022]	278.46 (-) [278.46]	12.06 (0.00) [0]
	BIHAR				
	Civil Aviation				
176	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II	5/2018	10/2022 (-) [3/2023]	1,216.90 (-) [1,216.90]	205.04 (0.00) [5]
	Human Resource Development				
177	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	2/2016	6/2017 (-) [10/2021]	496.18 (496.00) [498.99]	224.58 (2.81) [52]
178	PERMANENT CAMPUS FOR IIM BODH GAYA	9/2018	9/2020 (-) [11/2022]	375.00 (-) [375.00]	48.46 (0.00) [26]
	Petroleum				
179	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA	1/2020	4/2023 (-) [4/2023]	14,810.00 (-) [14,810.00]	934.70 (0.00) [0]
180	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA	10/2017	10/2022 (-) [10/2022]	359.25 (-) [359.25]	143.73 (0.00) [0]
181	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR	4/2018	3/2021 (12/2021) [12/2021]	522.00 (-) [522.00]	323.87 (0.00) [9]
182	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY	12/2017	10/2020 (8/2022) [8/2022]	199.36 (-) [199.36]	34.40 (0.00) [22]
183	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY	7/2018	1/2021 (6/2021) [6/2021]	189.00 (-) [189.00]	149.34 (0.00) [5]
184	LPG BP PROJECT MOTIHARI	5/2018	3/2021 (9/2021) [9/2021]	206.50 (-) [206.50]	134.97 (0.00) [6]
185	MUZAFFARPUR-MOTIHARI LPG PIPELINE	6/2020	8/2022 (-) [8/2022]	403.00 (-) [403.00]	1.77 (0.00) [0]
	Power				
186	BARH STPP(3X660MW) NTPC	2/2005	10/2011 (7/2023) [7/2023]	8,692.97 (21,312.11) [21,312.11]	18,595.56 (12,619.14) [141]
187	BRBCL-NABINAGAR TPP- JV (4X250 MW)	1/2007	7/2012 (6/2020) [7/2021]	5,353.00 (10,566.00) [10,566.00]	8,847.06 (5,213.00) [108]
188	BUXAR THERMAL POWER PLANT (1320 MW)	3/2019	1/2024 (-) [1/2024]	10,439.09 (10,439.09) [10,439.09]	2,035.50 (0.00) [0]
189	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	1/2013	5/2018 (-) [12/2021]	12,964.60 (17,304.00) [17,304.00]	15,787.92 (4,339.40) [43]
	Railways				
190	ARA-BHABHUA ROAD (NL)	4/2008	/ (-) [0/0]	633.87 (-) [633.87]	0.40 (0.00) [0]

191	ARARIA-SUPAUL (NL)	4/2008	/	1,605.17	53.52
			(-)	(-)	(0.00)
			[3/2023]	[1,605.17]	[-]
192	BIHTA-AURANGABAD (NL)	4/2008	/	326.20	2.08
			(-)	(-)	(2,668.81)
			[3/2024]	[2,995.01]	[-]
193	CHHAPRA-MUZAFFARPUR (NL)	4/2006	/	378.56	386.35
			(-)	(-)	(1,480.19)
			[3/2023]	[1,858.75]	[-]
194	DANIAWAN-BIHARSARIF (NL), ECR	4/2001	/	406.92	200.00
			(-)	(-)	(-67.92)
			[0/0]	[339.00]	[0]
195	DARBANGHA-KUSHESHWARSTHAN (NL)	4/2005	/	205.00	5.21
			(-)	(-)	(0.00)
			[0/0]	[205.00]	[0]
196	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	4/1991	/	329.39	1,207.52
			(-)	(-)	(1,153.75)
			[3/2022]	[1,483.14]	[-]
197	GAYA-DALTONGANJ VIA RAFIGANJ (NL)	4/2008	/	445.25	1.15
			(-)	(-)	(0.00)
			[0/0]	[445.25]	[0]
198	HAJIPUR-RAMDAYALUNAGAR DOUBLING	4/2013	/	213.01	486.66
			(-)	(-)	(266.99)
			[0/0]	[480.00]	[0]
199	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	4/2003	/	528.65	1,560.44
			(-)	(-)	(1,538.13)
			[3/2023]	[2,066.78]	[-]
200	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	4/1997	3/2012	324.73	1,069.58
			(-)	(-)	(745.27)
			[11/2022]	[1,070.00]	[128]
201	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	4/2009	3/2020	548.00	535.44
			(-)	(-)	(271.01)
			[3/2023]	[819.01]	[36]
202	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	4/1997	/	162.87	348.95
			(-)	(-)	(451.58)
			[12/2023]	[614.45]	[-]
203	KISHANGANJ JALALGARH, NL, NEFR	4/2008	/	333.76	6.74
			(-)	(-)	(26.24)
			[0/0]	[360.00]	[0]
204	KIUL - GAYA DOUBLING PROJECT	12/2015	3/2020	1,200.20	578.18
			(-)	(1,200.20)	(0.00)
			[3/2023]	[1,200.20]	[36]
205	KOSI BRIDGE (NL), ECR	4/2002	3/2020	499.41	447.86
			(-)	(-)	(16.61)
			[0/0]	[516.02]	[0]
206	KURSELA-BIHARIGANJ (NL)	4/2008	/	192.56	0.39
			(-)	(-)	(0.00)
			[0/0]	[192.56]	[0]
207	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	4/1996	3/2012	477.88	694.88
			(-)	(283.95)	(273.67)
			[7/2021]	[751.55]	[112]
208	MOTIHARI-SITAMARHI (NL)	4/2006	/	211.00	24.16
			(-)	(-)	(795.00)
			[0/0]	[1,006.00]	[0]
209	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM	4/2016	3/2021	731.64	217.95
			(-)	(-)	(454.09)
			[6/2022]	[1,185.73]	[15]
210	MUZAFFARPUR-DARBANGHA (NL)	4/2008	/	281.30	0.60
			(-)	(-)	(0.00)
			[0/0]	[281.30]	[0]
211	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL)	4/2008	/	228.05	1.53

			(-) [3/2024]	(-) [228.05]	(0.00) [-]
212	MUZAFFARPUR-SITAMARHI NEW LINE	1/1991	7/2014 (-) [0/0]	332.15 (-) [546.71]	541.43 (214.56) [0]
213	NAWADA-LAXMIPUR (NL)	4/2008	/ (-) [0/0]	620.57 (-) [620.57]	0.31 (0.00) [0]
214	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	9/2006	3/2019 (-) [3/2024]	532.87 (2,132.03) [2,145.00]	1,001.65 (1,612.13) [60]
215	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR	4/1998	/ (-) [0/0]	180.82 (-) [726.31]	546.29 (545.49) [0]
216	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	12/2015	3/2020 (-) [3/2023]	1,491.47 (-) [1,491.47]	508.88 (0.00) [36]
217	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM	4/2016	3/2021 (-) [3/2024]	744.04 (-) [1,215.54]	426.72 (471.50) [36]
218	SAKRI-HASANPUR ROAD (NL)	4/1999	/ (-) [3/2021]	325.00 (-) [735.20]	384.25 (410.20) [0]
219	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	4/2004	/ (-) [3/2023]	372.14 (-) [1,470.50]	1,288.24 (1,098.36) [-]
220	SAMASTIPUR-DARBANGHA	5/2015	/ (-) [3/2025]	380.00 (-) [519.33]	282.65 (139.33) [-]
221	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)	4/2008	/ (-) [0/0]	678.62 (-) [678.62]	17.20 (0.00) [0]
	Road Transport And Highways				
222	2 LANNING OF MUZAFFARPUR - SONBARSA	5/2011	11/2013 (12/2020) [1/2021]	511.54 (585.00) [591.00]	575.99 (79.46) [0]
223	2-LANNING WITH PS MOTIHARI-RAXAUL	10/2011	4/2014 (-) [0/0]	375.09 (-) [375.09]	494.33 (0.00) [0]
224	4-LANNING OF CHAPRA-HAJIPUR	1/2011	7/2013 (-) [0/0]	575.00 (-) [575.00]	555.63 (0.00) [0]
225	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ	5/2015	5/2017 (-) [0/0]	581.84 (-) [581.84]	89.69 (0.00) [0]
226	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA	10/2013	11/2020 (-) [0/0]	464.09 (-) [464.09]	0.00 (0.00) [0]
227	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT	10/2013	12/2020 (-) [0/0]	649.90 (-) [649.90]	0.00 (0.00) [0]
228	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE	10/2013	11/2020 (-) [0/0]	446.97 (-) [446.97]	0.00 (0.00) [0]
229	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00	2/2019	/ (-) [0/0]	2,926.42 (-) [2,926.42]	2.00 (0.00) [0]
230	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND	9/2018	/ (-) [0/0]	1,478.40 (-) [1,478.40]	1.98 (0.00) [0]
231	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM	8/2015	11/2015	288.24	303.16

	124/175 TO 140/200 OF NH-80 UNDER EPC MODE		(-) [0/0]	(-) [288.24]	(0.00) [0]
232	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15	12/2017	/	2,598.00	0.00
			(-) [0/0]	(-) [2,598.00]	(0.00) [0]
233	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE	3/2017	3/2020 (-) [5/2021]	235.48 (-) [227.77]	36.08 (-7.71) [14]
234	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER	3/2018	/	496.20	38.11
			(-) [0/0]	(-) [537.17]	(40.97) [0]
235	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	11/2013	7/2016 (-) [0/0]	683.83 (-) [560.70]	671.96 (-123.13) [0]
236	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016 (-) [0/0]	553.30 (-) [478.35]	289.14 (-74.95) [0]
237	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	6/2016 (-) [0/0]	369.77 (-) [369.77]	0.00 (0.00) [0]
238	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016 (-) [0/0]	178.85 (-) [152.62]	116.49 (-26.23) [0]
239	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31	12/2015	/	1,167.45	186.70
			(-) [0/0]	(-) [1,182.94]	(15.49) [0]
240	FOUR LANING OF BHOJPUR TO BUXAR	1/1991	/	642.41	400.60
			(-) [0/0]	(-) [681.67]	(39.26) [0]
241	FOUR LANING OF FORBESGANJ - JOGBANI	8/2015	4/2018 (-) [12/2020]	322.09 (-) [322.09]	77.53 (0.00) [0]
242	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR	1/2014	10/2016 (-) [0/0]	1,408.85 (-) [925.87]	745.25 (-482.98) [0]
243	FOUR LANING OF KOILWAR TO BHOJPUR	8/2015	/	814.04	512.04
			(-) [10/2021]	(-) [825.17]	(11.13) [-]
244	FOUR LANING OF PATNA TO KOILWAR	8/2015	/	556.07	0.00
			(-) [0/0]	(-) [556.07]	(0.00) [0]
245	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31	12/2015	4/2019 (-) [0/0]	1,041.10 (-) [1,041.10]	343.52 (0.00) [0]
246	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	9/2011	3/2014 (-) [0/0]	574.00 (-) [574.00]	768.73 (0.00) [0]
247	PATNA-MUZZAFFARPUR	8/2010	2/2013 (-) [0/0]	671.30 (-) [671.30]	1,360.63 (0.00) [0]
248	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM	8/2016	12/2016 (-) [0/0]	1,742.01 (-) [1,742.01]	1,233.39 (0.00) [0]
249	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I	1/2018	/	573.70	44.46
			(-) [0/0]	(-) [573.70]	(0.00) [0]
250	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH	10/2013	8/2014 (-) [0/0]	278.39 (-) [278.39]	0.00 (0.00) [0]
251	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	1/1991	/	478.35	458.03
			(-)	(-)	(0.00)

			[0/0]	[478.35]	[0]
252	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	1/1991	/ (-) [0/0]	319.68 (-) [369.77]	249.55 (50.09) [0]
253	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING	2/2014	7/2016 (-) [0/0]	665.50 (-) [665.50]	0.00 (0.00) [0]
254	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	1/1991	8/2016 (-) [0/0]	282.41 (-) [322.01]	327.21 (39.60) [0]
255	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	1/1991	10/2016 (-) [0/0]	358.22 (-) [377.64]	339.86 (19.42) [0]
256	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	1/1991	/ (-) [0/0]	675.00 (-) [675.00]	294.01 (0.00) [0]
257	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHI KM 40	1/1991	/ (-) [0/0]	154.62 (-) [154.62]	0.00 (0.00) [0]
258	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION	1/2018	/ (-) [0/0]	895.39 (-) [895.39]	0.00 (0.00) [0]
259	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	8/2017	8/2017 (-) [2/2022]	950.64 (-) [950.64]	200.18 (0.00) [54]
260	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH	3/2018	/ (-) [0/0]	153.24 (-) [153.24]	72.51 (0.00) [0]
261	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPR	3/2015	7/2016 (-) [0/0]	206.80 (-) [206.80]	74.04 (0.00) [0]
262	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA	8/2015	4/2019 (-) [0/0]	399.54 (-) [297.27]	271.39 (-102.27) [0]
263	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ	8/2015	/ (-) [0/0]	854.80 (-) [1,038.56]	1,160.00 (183.76) [0]
264	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR	8/2015	4/2018 (-) [0/0]	516.13 (-) [649.27]	712.15 (133.14) [0]
265	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN	3/2017	3/2020 (-) [0/0]	672.89 (-) [736.01]	31.82 (63.12) [0]
266	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC	5/2014	8/2016 (-) [0/0]	199.98 (-) [199.98]	174.35 (0.00) [0]
267	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C	11/2016	10/2019 (-) [0/0]	230.34 (-) [230.34]	210.12 (0.00) [0]
	<u>Urban Development</u>				
268	PATNA METRO RAIL CORPORATION LIMITED	2/2019	6/2024 (-) [6/2024]	13,365.77 (-) [13,365.77]	231.97 (0.00) [0]
	<u>Water Resources</u>				
269	I AND D AND STP AT CHAPRA	11/2018	12/2020 (6/2021) [4/2021]	236.15 (-) [236.15]	46.50 (0.00) [4]
270	I AND D AND STP WORKS FOR BHAGALPUR	10/2017	9/2020 (-) [0/0]	254.13 (-) [254.13]	0.05 (0.00) [0]
271	IRRIGATION WORK OF BAGMATI	10/2005	3/2015	956.00	712.37

			(-) [0/0]	(-) [721.37]	(-234.63) [0]
272	SAIDPUR SEWER NETWORK PATNA	4/2015	1/2021 (-) [0/0]	268.63 (-) [268.63]	296.97 (0.00) [0]
273	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR	4/2015	4/2020 (-) [6/2021]	184.93 (-) [184.93]	163.36 (0.00) [14]
274	SEWER NETWORK SPS AND STP BEGUSARAI	3/2018	7/2021 (-) [7/2021]	230.06 (-) [230.06]	73.63 (0.00) [0]
275	SEWER NETWORKS SPS AND STP HAJIPUR	3/2018	8/2021 (-) [12/2021]	305.19 (-) [305.19]	0.00 (0.00) [4]
276	SEWER NETWORKS, SPS AND STP, MUNGER	3/2018	10/2021 (-) [10/2021]	294.02 (-) [294.02]	0.00 (0.00) [0]
277	SEWERAGE SCHEME AT PAHARI ZONE IVA S PATNA	5/2017	5/2021 (-) [5/2021]	184.86 (-) [184.86]	152.78 (0.00) [0]
278	SEWERAGE SCHEME AT PAHARI ZONE V PATNA	5/2017	4/2021 (-) [4/2021]	356.37 (-) [356.37]	93.34 (0.00) [0]
279	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA	8/2017	6/2022 (-) [6/2022]	824.00 (-) [824.00]	40.09 (0.00) [0]
280	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA	8/2017	6/2022 (-) [6/2022]	578.89 (-) [578.89]	40.09 (0.00) [0]
281	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	3/2020 (-) [3/2021]	225.77 (-) [225.77]	276.57 (0.00) [0]
282	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK	3/2017	5/2021 (-) [5/2021]	277.42 (-) [277.42]	146.23 (0.00) [0]
283	SEWERAGE TREATMENT PLANT AT PAHARI PATNA	5/2017	11/2020 (3/2021) [0/0]	191.62 (-) [191.62]	54.96 (0.00) [0]
	CHANDIGARH				
	Road Transport And Highways				
284	WIDENING OF SL TO 2 L KM. 107-184.80 SUKUMA TO KONTA ON NH 221	3/2010	3/2013 (5/2019) [0/0]	179.89 (271.00) [271.00]	270.91 (91.11) [0]
285	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1	12/2010	1/2019 (-) [0/0]	169.26 (299.00) [299.00]	0.00 (129.74) [0]
	CHHATISGARH				
	Coal				
286	AMERA OC RCE	2/2015	3/2018 (-) [3/2023]	335.97 (-) [335.97]	49.49 (0.00) [60]
287	AMGAON OPENCAST PROJECT RCE	7/2015	3/2020 (-) [3/2023]	316.10 (-) [316.10]	141.02 (0.00) [36]
288	BAROUD OC EXPANSION (3-10 MTY)	8/2020	3/2029 (-) [3/2029]	2,309.80 (-) [2,309.80]	275.61 (0.00) [0]
289	CHHAL OC SEAM -III (6.00 MTY)	12/2013	3/2022 (-) [3/2022]	610.63 (-) [610.63]	152.93 (0.00) [0]
290	DIPKA OC EXPANSION 40 MTY	12/2020	3/2029	5,241.40	1,931.58

			(-) [3/2029]	(-) [5,241.40]	(0.00) [0]
291	DURGAPUR OPENCAST PROJECT	2/2015	3/2023 (-) [3/2026]	916.24 (-) [916.24]	11.38 (0.00) [36]
292	GEVRA EXPANSION OCP (SECL) (35-70) MTY	6/2010	3/2023 (3/2016) [3/2023]	11,816.40 (-) [11,816.40]	4,487.05 (0.00) [0]
293	JAGANNATHPOR OCP(3.00MTY)	9/2008	3/2015 (3/2020) [3/2022]	152.43 (459.49) [459.49]	202.90 (307.06) [84]
294	JAMPALI OCP RCE	5/2020	3/2024 (-) [3/2024]	278.64 (-) [278.64]	183.02 (0.00) [0]
295	JHIRIA WEST OPENCAST PROJECT	11/2018	3/2026 (-) [3/2026]	389.97 (-) [389.97]	0.00 (0.00) [0]
296	KARTALI (EAST) OCP (2.50 MTY)	7/2008	3/2014 (-) [3/2022]	178.44 (-) [178.44]	6.50 (0.00) [96]
297	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY	8/2013	3/2023 (-) [3/2023]	7,612.33 (-) [7,612.33]	2,745.45 (0.00) [0]
298	MADANNAGAR OPENCAST PROJECT	10/2015	3/2024 (-) [3/2024]	1,875.32 (-) [1,875.32]	0.00 (0.00) [0]
299	MAHAMAYA OPENCAST PROJECT	5/2018	3/2026 (-) [3/2026]	410.26 (-) [410.26]	28.26 (0.00) [0]
300	MANIKPUR OC EXPANSION (3.5 MTY)	12/2009	3/2014 (-) [3/2021]	321.50 (-) [321.50]	211.38 (0.00) [0]
301	PELMA OCP(15.00MTY)	11/2014	3/2023 (-) [3/2023]	1,624.59 (-) [1,624.59]	9.09 (0.00) [0]
302	PORDA CHIMTAPANI OCP (10 MTY)	12/2020	3/2029 (-) [3/2029]	2,310.12 (-) [2,310.12]	0.00 (0.00) [0]
303	VIJAY WEST OPENCAST PROJECT	5/2017	3/2026 (-) [3/2026]	976.95 (-) [976.95]	75.96 (0.00) [0]
	<u>Human Resource Development</u>				
304	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I.	3/2020	7/2022 (-) [7/2022]	808.62 (-) [808.62]	57.42 (0.00) [0]
	<u>Power</u>				
305	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	12/2012	10/2017 (-) [0/0]	11,846.00 (-) [12,739.82]	13,766.78 (893.82) [0]
306	TALAIPALLI COAL MINING PROJECT	9/2015	11/2019 (-) [0/0]	3,004.00 (-) [3,004.00]	2,464.37 (0.00) [0]
	<u>Railways</u>				
307	CHAMPA-JHARSUGUDA 3RD LINE	4/2008	12/2019 (-) [0/0]	872.00 (-) [1,226.51]	1,131.91 (354.51) [0]
308	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW	2/2016	3/2020 (-) [6/2021]	393.98 (-) [393.98]	350.81 (0.00) [15]
309	GEVRA ROAD PENDRA ROAD	2/2014	3/2022 (-)	2,288.00 (-)	866.16 (2,682.11)

			[12/2023]	[4,970.11]	[21]
310	JHARSUGUDA-BILASPUR 4TH LINE	4/2015	3/2021 (-) [12/2023]	1,973.00 (-) [2,135.34]	351.35 (162.34) [33]
311	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	4/2013	9/2018 (-) [3/2022]	3,055.00 (-) [3,055.15]	2,431.72 (0.15) [42]
312	KIRANDUL - JAGDALPUR DOUBLING	12/2012	3/2020 (3/2023) [3/2023]	1,160.00 (1,160.83) [1,160.83]	950.18 (0.83) [36]
313	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR	5/2014	3/2018 (-) [0/0]	207.00 (-) [207.00]	153.83 (0.00) [0]
314	RAIPUR - TITLAGARH - DOUBLING	3/2007	3/2020 (-) [12/2021]	1,402.02 (-) [1,300.00]	1,294.72 (-102.02) [21]
	<u>Road Transport And Highways</u>				
315	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF	3/2018	/ (-) [3/2021]	1,029.96 (-) [1,261.05]	197.88 (231.09) [0]
316	FOUR LANING OF SARAGAON - BILASPUR	12/2015	4/2018 (-) [0/0]	509.13 (-) [509.13]	412.66 (0.00) [0]
317	FOUR LANING OF SIMGA - SARAGAON	12/2015	5/2018 (-) [0/0]	596.67 (-) [596.67]	426.38 (0.00) [0]
318	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION.	12/2015	/ (6/2021) [6/2021]	291.05 (-) [291.05]	212.46 (0.00) [-]
319	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION	11/2015	6/2017 (6/2021) [6/2021]	335.32 (-) [335.32]	269.15 (0.00) [48]
320	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 127.500 TO 178.944 DARRIGHAT TO BANARI SECTION	3/2016	9/2016 (10/2020) [10/2020]	491.52 (512.77) [491.52]	474.52 (0.00) [0]
321	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V	1/2016	9/2016 (6/2021) [6/2021]	476.20 (543.73) [544.00]	400.38 (67.80) [57]
322	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION	12/2014	3/2015 (6/2021) [6/2021]	496.02 (-) [496.02]	240.11 (0.00) [75]
323	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180	1/2016	8/2016 (6/2021) [6/2021]	497.14 (572.66) [572.66]	270.56 (75.52) [58]
324	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	1/2016	10/2016 (6/2021) [6/2021]	624.98 (731.50) [731.50]	416.16 (106.52) [56]
325	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI	3/2016	7/2016 (6/2021) [6/2021]	452.94 (435.61) [435.61]	94.34 (-17.33) [59]
326	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO	3/2017	1/2018 (3/2021) [3/2021]	423.79 (-) [423.79]	273.27 (0.00) [0]
327	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION	11/2015	12/2015 (5/2020) [5/2020]	485.44 (-) [485.44]	447.13 (0.00) [0]
328	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A	11/2017	5/2019 (6/2021) [6/2021]	188.80 (-) [188.80]	78.69 (0.00) [25]
329	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331	12/2014	11/2017 (6/2021)	379.16 (-)	272.43 (0.00)

			[6/2021]	[379.16]	[43]
	<u>Steel</u>				
330	NMDC INTEGRATED STEEL PLANT	1/2010	5/2015 (7/2021) [7/2021]	15,525.00 (21,940.00) [21,940.00]	18,516.49 (6,415.00) [74]
331	NMDC SLURRY PIPE LINE PROJECT - PHASE-1	11/2015	6/2023 (-) [6/2023]	2,907.00 (-) [2,907.00]	256.24 (0.00) [0]
332	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP	11/2020	12/2023 (-) [12/2023]	542.24 (-) [542.24]	31.68 (0.00) [0]
	<u>Urban Development</u>				
333	CONSTRUCTION 729 QUARTERS (TYPE II-180, TYPE III-364, TYPE IV-112, TYPE V-68, TYPE VI-5), SHOPS, CO	5/2019	9/2020 (-) [0/0]	299.97 (-) [299.97]	0.29 (0.00) [0]
	<u>DELHI</u>				
	<u>Civil Aviation</u>				
334	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	11/2016	4/2020 (-) [3/2022]	303.80 (351.21) [303.80]	167.55 (0.00) [23]
	<u>Commerce</u>				
335	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI	6/2018	10/2020 (-) [0/0]	302.64 (-) [302.64]	60.00 (0.00) [0]
	<u>Dpiit</u>				
336	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	12/2019 (-) [12/2021]	4,773.00 (-) [5,178.00]	2,557.37 (405.00) [24]
	<u>Health And Family Welfare</u>				
337	AIIMS - MOTHER AND CHILD BLOCK	12/2013	5/2017 (-) [3/2021]	204.44 (-) [250.00]	240.24 (45.56) [0]
338	AIIMS - OPD(NEW)	8/2014	5/2017 (-) [1/2020]	293.65 (-) [325.00]	299.76 (31.35) [0]
339	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	/ (-) [6/2021]	156.56 (-) [190.34]	143.14 (33.78) [-]
340	LHMC NEW DELHI-RE-DEVELOPMENT	2/2013	11/2013 (-) [5/2021]	414.11 (-) [499.23]	494.72 (85.12) [90]
	<u>Heavy Industry</u>				
341	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	8/2016	9/2019 (-) [0/0]	1,554.00 (-) [900.00]	815.00 (-654.00) [0]
	<u>Home Affairs</u>				
342	BUILDING OF THE FORCE HEADQUARTER INCLUDING SECTOR HQ RAF	6/2019	7/2022 (-) [7/2022]	277.35 (-) [277.35]	10.60 (0.00) [0]
343	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	10/2019 (-) [12/2021]	1,219.21 (-) [2,000.00]	906.04 (780.79) [26]
	<u>Power</u>				
344	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	10/2017	11/2019 (-) [6/2021]	271.90 (-) [271.90]	240.96 (0.00) [19]
345	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	3/2015	5/2017 (9/2021) [9/2021]	1,394.52 (-) [1,394.52]	534.89 (0.00) [52]
	<u>Railways</u>				
346	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE	4/2012	/	295.68	127.91

			(-) [9/2023]	(-) [419.00]	(123.32) [-]
347	GRADE SEPERATOR AT DAYABASTI	4/1999	/	156.65	111.51
			(-) [3/2024]	(-) [359.00]	(202.35) [-]
	<u>Road Transport And Highways</u>				
348	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8	7/2017	9/2019 (-) [0/0]	269.69 (-) [269.69]	0.00 (0.00) [0]
	<u>Rural Development</u>				
349	CONSTRUCTION OF GRAMEEN VIKAS BHAWAN (2BASEMENTS+ GROUND+9 FLOORS) FOR MINISTRY OF RURAL DEVELOPMENT	11/2018	7/2021 (-) [7/2021]	361.60 (-) [361.60]	12.44 (0.00) [0]
	<u>Telecommunications</u>				
350	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	10/2016	3/2018 (-) [6/2021]	248.20 (-) [248.20]	145.26 (0.00) [39]
	<u>Urban Development</u>				
351	C/O STEEL STRUCTURE BUILDINGS USING PRE-ENGINEERED TECHNOLOGY AT AFRICA AVENUE AND KG MARG	2/2020	11/2020 (-) [0/0]	532.00 (-) [532.00]	150.00 (0.00) [0]
352	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	6/2015	4/2019 (6/2021) [12/2021]	197.33 (-) [197.33]	106.16 (0.00) [32]
353	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI	7/2017	11/2020 (-) [0/0]	218.72 (-) [218.72]	126.16 (0.00) [0]
354	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	7/2012	12/2015 (-) [0/0]	884.30 (-) [884.30]	812.00 (0.00) [0]
355	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS	7/2019	3/2025 (-) [3/2025]	24,948.65 (-) [24,948.65]	1,763.02 (0.00) [0]
356	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND	5/2017	12/2020 (-) [9/2021]	565.00 (-) [565.00]	438.37 (0.00) [9]
357	DELHI MRTS PHASE-III	9/2011	3/2016 (-) [9/2021]	38,585.00 (-) [38,585.00]	39,182.53 (0.00) [66]
358	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B	11/2017	5/2020 (-) [0/0]	238.56 (-) [238.56]	157.67 (0.00) [0]
359	REDEVELOPMENT OF EAST KIDWAI NAGAR	6/2012	11/2019 (-) [0/0]	4,264.00 (-) [4,720.73]	4,683.08 (456.73) [0]
360	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I	10/2016	7/2021 (-) [12/2024]	1,180.00 (-) [1,100.80]	35.63 (-79.20) [41]
361	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N	10/2016	8/2020 (-) [3/2022]	392.00 (-) [392.00]	73.79 (0.00) [19]
362	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I	10/2016	3/2022 (-) [3/2022]	1,128.00 (-) [1,128.00]	22.00 (0.00) [0]
363	REDEVELOPMENT OF GPRA AT MOHAMMADPUR	10/2016	3/2021 (7/2021) [7/2021]	422.00 (-) [422.00]	70.75 (0.00) [4]
364	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR	7/2016	/	2,694.00	744.73
			(-) [12/2022]	(-) [2,694.00]	(0.00) [-]
	<u>Water Resources</u>				

365	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO	5/2017	5/2020 (-) [0/0]	344.81 (-) [344.81]	0.00 (0.00) [0]
366	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI	12/2018	1/2021 (-) [6/2021]	515.07 (-) [515.07]	336.27 (0.00) [5]
367	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L	3/2017	12/2022 (-) [12/2022]	665.78 (-) [665.78]	194.55 (0.00) [0]
368	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2	5/2016	12/2021 (-) [12/2022]	211.79 (-) [211.79]	87.31 (0.00) [12]
369	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S	5/2016	2/2022 (-) [12/2022]	239.11 (-) [239.11]	129.67 (0.00) [10]
	GOA				
	Health And Family Welfare				
370	SUPER SPECIALITY BLOCK PMSSY GOA	1/2018	/ (-) [1/2021]	249.01 (-) [249.07]	231.05 (0.06) [0]
	Human Resource Development				
371	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA.	5/2019	3/2020 (-) [0/0]	303.90 (-) [303.90]	17.00 (0.00) [0]
	Road Transport And Highways				
372	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE	3/2015	/ (-) [0/0]	280.16 (-) [290.59]	219.47 (10.43) [0]
373	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD	3/2015	/ (-) [0/0]	184.05 (-) [184.05]	91.39 (0.00) [0]
374	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE	10/2015	/ (-) [0/0]	936.40 (-) [936.40]	478.46 (0.00) [0]
375	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K	3/2015	/ (-) [0/0]	298.33 (-) [298.33]	310.72 (0.00) [0]
376	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE	3/2015	4/2018 (-) [0/0]	297.00 (-) [297.00]	290.64 (0.00) [0]
377	KARASWADA TO BAMBOLIM	3/2017	12/2019 (-) [0/0]	852.67 (-) [852.67]	138.14 (0.00) [0]
378	PATRADEVI TO KARASWADA 4L	3/2017	5/2020 (-) [0/0]	634.32 (-) [634.32]	278.30 (0.00) [0]
379	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER	12/2015	/ (-) [0/0]	773.98 (-) [773.98]	336.25 (0.00) [0]
380	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR	12/2015	/ (-) [0/0]	819.95 (-) [819.95]	205.20 (0.00) [0]
	GUJARAT				
	Atomic Energy				
381	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015 (-) [2/2022]	11,459.00 (-) [16,580.00]	16,488.00 (5,121.00) [74]
	Civil Aviation				
382	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT	1/2018	8/2022 (-) [8/2022]	1,405.00 (-) [1,405.00]	250.63 (0.00) [0]

	Petroleum				
383	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY	11/2019	5/2023 (-) [5/2023]	5,251.00 (-) [5,251.00]	192.50 (0.00) [0]
384	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT	3/2018	/ (5/2023) [5/2023]	588.20 (730.20) [730.20]	77.30 (142.00) [-]
385	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM	10/2020	8/2023 (-) [8/2023]	1,614.00 (-) [1,614.00]	0.00 (0.00) [0]
386	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	4/2016	4/2018 (-) [6/2021]	327.78 (-) [200.00]	196.50 (-127.78) [38]
387	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE	10/2017	2/2020 (10/2021) [10/2021]	906.00 (-) [906.00]	279.82 (0.00) [20]
388	LAB REVAMP AT GUJARAT REFINERY	10/2019	12/2021 (-) [12/2021]	403.00 (-) [403.00]	103.74 (0.00) [0]
389	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY	9/2020	9/2024 (-) [9/2024]	18,936.00 (-) [18,936.00]	715.09 (0.00) [0]
390	REDEVELOPMENT OF NANDASAN FIELD	2/2020	8/2022 (-) [8/2022]	444.87 (-) [444.87]	87.40 (0.00) [0]
391	REDEVELOPMENT OF SANTHAL FIELD	2/2017	3/2026 (-) [3/2026]	1,162.56 (-) [970.30]	832.63 (-192.26) [0]
392	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END	6/2020	12/2022 (-) [12/2022]	1,378.00 (-) [1,378.00]	24.39 (0.00) [0]
393	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI	9/2018	2/2021 (-) [12/2021]	225.54 (247.90) [247.90]	40.10 (22.36) [10]
	Power				
394	KAWAS SOLAR 56 MW	8/2020	10/2021 (-) [10/2021]	261.80 (-) [261.80]	0.00 (0.00) [0]
395	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPG AT BANASKANTHA (RADHANESDA) GUJARAT	12/2017	6/2019 (11/2020) [9/2020]	193.14 (-) [193.14]	123.36 (0.00) [0]
396	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT	5/2017	9/2018 (11/2020) [9/2020]	175.64 (-) [175.64]	122.47 (0.00) [0]
	Railways				
397	AHMEDABAD-BOTAD (GC)	4/2012	12/2021 (-) [12/2021]	975.62 (-) [1,500.00]	1,497.74 (524.38) [0]
398	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	4/2008	3/2020 (3/2024) [3/2024]	829.74 (1,959.74) [1,959.74]	1,799.00 (1,130.00) [48]
399	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	4/2006	3/2011 (-) [0/0]	117.36 (196.95) [202.35]	809.40 (84.99) [0]
400	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	2/1991	3/2019 (10/2021) [10/2021]	551.51 (890.76) [890.76]	745.11 (339.25) [31]
401	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	4/2008	3/2012 (3/2023) [3/2023]	318.24 (411.62) [411.62]	126.05 (93.38) [132]
402	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION	4/2017	3/2020	691.84	719.56

	UPTO KEVADIYA(32.68KM) =49.75KM		(2/2021) [2/2021]	(1,017.91) [1,017.91]	(326.07) [0]
403	DHASA-JETALSAR (GC)	4/2012	3/2021 (-) [3/2021]	644.38 (-) [872.65]	800.30 (228.27) [0]
404	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO	3/2017	/ (-) [0/0]	243.60 (-) [243.60]	0.00 (0.00) [0]
405	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC)	4/2011	/ (3/2024) [3/2024]	844.10 (844.10) [844.10]	186.59 (0.00) [-]
406	MULTI MODAL LOGISTICS PARK AT VARNAMA	10/2013	3/2019 (-) [0/0]	343.00 (-) [343.00]	222.83 (0.00) [0]
407	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220	3/2012	/ (-) [0/0]	153.83 (-) [153.83]	0.00 (0.00) [0]
408	PALANPUR-SAMAKHAYALI (DL)	4/2013	12/2021 (-) [3/2022]	1,548.66 (-) [1,868.89]	1,831.45 (320.23) [3]
409	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	4/1994	3/2019 (3/2023) [3/2023]	320.66 (1,378.11) [1,378.11]	540.09 (1,057.45) [48]
410	SURENDRA NAGAR RAJKOT	4/2015	3/2021 (12/2022) [12/2022]	1,002.39 (1,002.39) [1,002.39]	653.86 (0.00) [21]
411	VIRAMGAM-SAMAKHIALI (DL)	4/2011	3/2021 (12/2021) [12/2021]	1,037.15 (1,389.05) [1,389.05]	1,125.73 (351.90) [9]
412	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON	3/2012	/ (-) [0/0]	248.26 (-) [248.26]	0.00 (0.00) [0]
	Road Transport And Highways				
413	2-LANE WITH PAVED SHOULDERS OF GADU- PORBANDER SECTION	12/2016	/ (-) [0/0]	417.19 (-) [417.19]	303.96 (0.00) [0]
414	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH- 8E FROM KM 221.610 TO KM 263.000	7/2016	/ (-) [0/0]	829.97 (-) [829.97]	248.88 (0.00) [0]
415	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT	6/2017	6/2020 (-) [2/2021]	1,958.88 (-) [1,993.81]	1,116.85 (34.93) [0]
416	AHMEDABAD TO VADODARA SECTION	1/2013	12/2015 (-) [0/0]	2,125.24 (-) [2,125.24]	4,669.71 (0.00) [0]
417	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS	5/2016	/ (-) [4/2021]	364.56 (-) [392.00]	353.42 (27.44) [-]
418	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR	3/2018	/ (-) [0/0]	1,161.39 (-) [1,161.39]	0.00 (0.00) [0]
419	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S	3/2018	/ (-) [7/2021]	1,437.64 (-) [1,437.64]	564.11 (0.00) [-]
420	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S	3/2018	/ (-) [6/2021]	2,702.05 (-) [2,043.00]	1,327.65 (-659.05) [-]
421	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPIR ODMA KHAVDA DHOLAVIRA MAUVANA	10/2018	5/2019 (-) [0/0]	400.76 (-) [400.76]	131.34 (0.00) [0]
422	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN	8/2017	3/2018	962.43	249.39

	DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU		(-) [0/0]	(-) [962.43]	(0.00) [0]
423	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE	12/2017	11/2018 (-) [0/0]	867.97 (-) [867.97]	516.24 (0.00) [0]
424	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6.	5/2016	/ (-) [0/0]	998.18 (-) [998.18]	719.75 (0.00) [0]
425	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST	5/2016	/ (-) [0/0]	723.64 (-) [723.64]	503.45 (0.00) [0]
426	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR	5/2016	/ (-) [0/0]	834.64 (-) [834.64]	203.40 (0.00) [0]
427	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU	5/2016	/ (-) [0/0]	763.08 (-) [763.08]	450.54 (0.00) [0]
428	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	3/2010	9/2012 (-) [0/0]	1,509.10 (-) [1,509.10]	3,684.44 (0.00) [0]
429	JUNAGADH BYPASS	10/2017	10/2017 (-) [0/0]	232.49 (-) [232.49]	0.00 (0.00) [0]
430	KANDLA - MUNDRA PORT	1/2011	7/2013 (-) [0/0]	953.88 (-) [953.88]	976.79 (0.00) [0]
431	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF	2/2018	/ (-) [1/2021]	1,052.21 (-) [1,449.00]	342.39 (396.79) [0]
432	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG.	1/2017	/ (-) [0/0]	1,251.11 (-) [1,251.11]	1,084.26 (0.00) [0]
433	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME	5/2016	/ (-) [0/0]	425.60 (-) [425.60]	134.77 (0.00) [0]
434	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4	3/2018	6/2021 (-) [6/2021]	351.00 (-) [351.00]	128.70 (0.00) [0]
435	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEE	3/2018	11/2018 (-) [0/0]	464.07 (-) [464.07]	302.02 (0.00) [0]
436	VADODARA-SURAT SECTION	3/2014	8/2016 (-) [0/0]	503.16 (-) [503.16]	389.50 (0.00) [0]
	<u>Urban Development</u>				
437	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	12/2018 (-) [8/2022]	10,773.00 (-) [12,787.00]	8,768.08 (2,014.00) [44]
438	AHMEDABAD METRO RAIL PROJECT PHASE II	3/2019	3/2024 (-) [3/2024]	5,384.17 (-) [5,384.17]	63.77 (0.00) [0]
439	SURAT METRO RAIL PROJECT	3/2019	3/2024 (-) [3/2024]	12,020.32 (-) [12,020.32]	20.65 (0.00) [0]
	<u>HARYANA</u>				
	<u>Fertilisers</u>				
440	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT	1/2018	11/2019 (6/2021) [5/2021]	215.92 (-) [215.92]	168.30 (0.00) [18]
	<u>Health And Family Welfare</u>				
441	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI	9/2014	3/2018	505.58	586.96

	JHAJJAR		(-) [9/2019]	(-) [585.00]	(79.42) [0]
	<u>Home Affairs</u>				
442	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE-	1/2020	10/2023 (-) [10/2023]	166.98 (167.00) [166.98]	0.00 (0.00) [0]
443	CONSTRUCTION OF SEPARATE FAMILY ACCOMMODATION (440 NOS.) (PHASE- C/O 336 NOS. TYPE- II QTRS , 96	1/2020	5/2022 (-) [5/2022]	166.98 (-) [166.98]	0.29 (0.00) [0]
	<u>Petroleum</u>				
444	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY	1/2019	1/2021 (3/2022) [3/2022]	909.00 (-) [909.00]	309.94 (0.00) [14]
445	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	4/2018	2/2020 (8/2021) [8/2021]	206.63 (-) [206.63]	93.11 (0.00) [18]
446	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS	9/2018	9/2026 (2/2027) [2/2027]	520.00 (-) [520.00]	126.72 (0.00) [5]
447	COMPRESSED BIO GAS PLANT AT GORAKHPUR	9/2019	7/2021 (3/2022) [3/2022]	164.69 (-) [164.69]	13.16 (0.00) [8]
448	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA	11/2017	11/2020 (6/2021) [6/2021]	255.00 (300.00) [300.00]	271.70 (45.00) [7]
449	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY	10/2018	2/2020 (2/2022) [2/2022]	598.00 (-) [598.00]	293.80 (0.00) [24]
450	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT	12/2018	6/2021 (7/2022) [7/2022]	278.60 (-) [278.60]	44.73 (0.00) [13]
451	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT	8/2018	8/2020 (4/2022) [4/2022]	1,636.00 (-) [1,636.00]	723.59 (0.00) [20]
452	PX-PTA REVAMP AT PANIPAT REFINERY	8/2019	10/2021 (-) [10/2021]	1,255.00 (-) [1,255.00]	185.11 (0.00) [0]
453	R and D CAMPUS II AT FARIDABAD	6/2019	12/2022 (7/2023) [7/2023]	2,281.94 (-) [2,281.94]	431.31 (0.00) [7]
454	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT	8/2018	8/2020 (5/2021) [6/2021]	286.42 (327.01) [327.01]	186.00 (40.59) [10]
	<u>Railways</u>				
455	MULTI MODAL LOGISTICS PARK AT BARHI	12/2015	3/2019 (-) [3/2021]	346.32 (-) [346.32]	320.28 (0.00) [0]
456	ROHTAK-MEHAM HANSI	4/2012	12/2011 (-) [6/2021]	287.00 (-) [893.45]	705.53 (606.45) [114]
	<u>Road Transport And Highways</u>				
457	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	12/2015	6/2016 (-) [0/0]	602.95 (-) [507.70]	496.22 (-95.25) [0]
458	4 LANING OF AMBALA - KAITHAL - PACKAGE -2	1/2016	7/2018 (-) [0/0]	574.28 (-) [537.16]	516.32 (-37.12) [0]
459	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL	3/2017	3/2020 (5/2021) [5/2021]	639.79 (-) [552.90]	597.77 (-86.89) [14]
460	8 LANING OF MUKARBA CHOWK TO PANIPAT	7/2015	4/2019	2,128.72	1,070.00

			(-) [9/2021]	(-) [2,128.72]	(0.00) [29]
461	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC)	1/2017	3/2019 (-) [0/0]	276.01 (-) [276.01]	187.39 (0.00) [0]
462	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS	1/2017	3/2019 (-) [2/2021]	247.25 (-) [247.25]	178.64 (0.00) [0]
463	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73	8/2016	5/2019 (-) [0/0]	248.97 (-) [248.97]	270.65 (0.00) [0]
464	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P	3/2018	/ (6/2021) [12/2020]	1,484.30 (-) [1,484.30]	165.51 (0.00) [0]
465	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211	9/2016	5/2019 (-) [0/0]	1,004.67 (-) [813.45]	577.21 (-191.22) [0]
466	DELHI/ HARYANA BORDER TO ROHTAK	4/2007	5/2010 (-) [0/0]	486.00 (-) [486.00]	470.01 (0.00) [0]
467	ISMAILABAD-NARNAUL PKG-1	1/2019	/ (-) [0/0]	996.65 (-) [996.65]	567.52 (0.00) [0]
468	ISMAILABAD-NARNAUL PKG-2	1/2019	/ (-) [0/0]	1,243.45 (-) [1,243.45]	659.79 (0.00) [0]
469	ISMAILABAD-NARNAUL PKG-3	1/2019	/ (-) [0/0]	889.36 (-) [889.36]	438.38 (0.00) [0]
470	ISMAILABAD-NARNAUL PKG-4	1/2019	/ (-) [0/0]	1,018.79 (-) [1,018.79]	468.24 (0.00) [0]
471	ISMAILABAD-NARNAUL PKG-5	1/2019	/ (-) [0/0]	1,051.91 (-) [1,051.91]	526.09 (0.00) [0]
472	ISMAILABAD-NARNAUL PKG-6	1/2019	/ (-) [0/0]	1,120.06 (-) [1,120.06]	501.73 (0.00) [0]
473	ISMAILABAD-NARNAUL PKG-7	1/2019	/ (-) [0/0]	1,137.42 (-) [1,137.42]	690.88 (0.00) [0]
474	ISMAILABAD-NARNAUL PKG-8	1/2019	/ (-) [0/0]	1,033.19 (-) [1,033.19]	604.45 (0.00) [0]
475	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	5/2009	11/2011 (-) [0/0]	1,108.00 (-) [2,967.50]	3,996.01 (1,859.50) [0]
476	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS	3/2018	/ (-) [0/0]	551.58 (-) [551.58]	306.06 (0.00) [0]
477	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE	3/2018	/ (-) [0/0]	275.12 (-) [275.12]	167.13 (0.00) [0]
478	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTING	3/2018	/ (-) [0/0]	307.79 (-) [307.79]	197.30 (0.00) [0]
479	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN	3/2018	/ (-) [0/0]	181.78 (-) [181.78]	129.84 (0.00) [0]
480	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM	3/2018	/ (-)	198.05 (-)	116.46 (0.00)

	DESIGN CHAIN		[0/0]	[198.05]	[0]
481	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I)	3/2018	/ (-) [7/2021]	795.50 (-) [799.30]	213.17 (3.80) [-]
482	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA	3/2018	/ (-) [7/2021]	634.70 (-) [931.21]	268.17 (296.51) [-]
	HIMACHAL PRADESH				
	Health And Family Welfare				
483	AIIMS BILASPUR	4/2018	9/2021 (-) [9/2021]	1,351.00 (-) [1,471.00]	712.04 (120.00) [0]
484	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH	12/2018	6/2021 (-) [5/2022]	260.00 (-) [260.00]	25.38 (0.00) [11]
	Human Resource Development				
485	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	11/2012	11/2014 (-) [0/0]	270.83 (-) [270.83]	226.16 (0.00) [0]
486	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR	9/2018	6/2022 (-) [6/2022]	392.51 (-) [392.51]	38.44 (0.00) [0]
	Power				
487	LUHRI HYDROELECTRIC PROJECT (STAGE1)	11/2020	1/2026 (-) [1/2026]	1,810.56 (-) [1,810.56]	422.46 (0.00) [0]
488	PARBATI HEP (4X200 MW) (NHPC) II	9/2002	9/2009 (7/2022) [7/2022]	3,919.59 (9,897.59) [9,897.59]	8,945.10 (5,978.00) [154]
	Railways				
489	BHANUPALI-BILASPUR BERI NL	4/2008	12/2026 (-) [12/2025]	2,966.99 (-) [6,753.42]	926.84 (3,786.43) [-12]
	Road Transport And Highways				
490	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345)	2/2016	2/2019 (-) [0/0]	273.20 (-) [273.20]	667.10 (0.00) [0]
491	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P	6/2017	6/2020 (-) [9/2021]	2,485.93 (-) [2,485.93]	827.64 (0.00) [15]
492	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM)	11/2013	11/2016 (-) [0/0]	1,916.79 (-) [1,916.79]	1,960.92 (0.00) [0]
493	FOUR LANING OF PARWANOO -SOLAN	9/2015	3/2018 (-) [0/0]	934.46 (-) [934.46]	697.33 (0.00) [0]
494	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M	3/2018	/ (-) [5/2021]	478.74 (-) [478.74]	127.42 (0.00) [-]
495	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH	9/2016	/ (-) [0/0]	1,273.71 (-) [1,273.71]	663.25 (0.00) [0]
496	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000)	10/2016	/ (-) [8/2020]	447.75 (-) [447.75]	1,160.74 (0.00) [0]
497	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS	8/2016	/ (-) [0/0]	1,583.18 (-) [1,583.18]	271.06 (0.00) [0]
	JAMMU AND KASHMIR				
	Civil Aviation				
498	CONSTRUCTION OF TERMINAL BUILDING AND	7/2018	9/2021	346.27	51.11

	ASSOCIATED WORKS AT LEH AIRPORT		(-) [9/2021]	(-) [480.33]	(134.06) [0]
	<u>Health And Family Welfare</u>				
499	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR	3/2019	9/2025 (-) [5/2024]	1,828.00 (-) [1,828.00]	0.00 (0.00) [-16]
500	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR	3/2019	9/2025 (-) [9/2025]	1,577.00 (-) [1,828.00]	0.00 (251.00) [0]
501	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR	3/2019	9/2023 (-) [9/2023]	1,404.00 (-) [1,404.00]	200.58 (0.00) [0]
	<u>Human Resource Development</u>				
502	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C)	1/2018	4/2023 (-) [4/2023]	676.00 (-) [676.00]	0.00 (0.00) [0]
503	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1)	3/2019	7/2022 (-) [7/2022]	329.00 (-) [329.00]	0.00 (0.00) [0]
	<u>Power</u>				
504	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	10/2014	4/2020 (-) [7/2025]	8,112.12 (-) [8,112.12]	1,766.91 (0.00) [63]
	<u>Railways</u>				
505	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	3/1995	11/2002 (-) [12/2022]	2,500.00 (-) [27,949.00]	24,040.61 (25,449.00) [241]
	<u>Road Transport And Highways</u>				
506	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D	8/2020	9/2026 (-) [9/2026]	6,808.69 (-) [6,808.69]	0.00 (0.00) [0]
507	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE	12/2017	/ (-) [1/2021]	1,471.75 (1,339.00) [1,339.00]	862.50 (-132.75) [0]
508	CONSTRUCTION, OPERATION AND MAINTENANCE OF Z-MORH TUNNEL INCLUDING APPROACHES ON NH-01 SRINAGAR-SONA	12/2019	12/2023 (-) [12/2023]	2,680.42 (-) [2,680.42]	0.00 (0.00) [0]
509	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A	12/2015	6/2019 (-) [12/2020]	2,168.66 (-) [2,168.66]	816.46 (0.00) [0]
510	FOUR LANING OF UDHAMPUR - RAMBAN SECTION OF NH-1A	12/2015	12/2018 (-) [0/0]	2,136.97 (-) [2,136.97]	1,615.66 (0.00) [0]
511	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	7/2010	7/2013 (-) [0/0]	1,813.76 (-) [1,813.76]	2,652.11 (0.00) [0]
512	NASHRI- CHANANI	5/2011	6/2015 (-) [0/0]	2,159.00 (-) [2,519.00]	4,709.65 (360.00) [0]
513	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	7/2010	7/2015 (-) [9/2020]	1,987.00 (-) [1,987.00]	3,108.90 (0.00) [0]
514	SRINAGAR TO BANIHAL	6/2011	6/2014 (-) [10/2020]	1,100.70 (-) [1,100.70]	2,924.02 (0.00) [0]
515	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL	7/2020	4/2022 (-) [4/2022]	228.39 (-) [228.39]	0.00 (0.00) [0]
516	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K	7/2020	4/2022 (-) [4/2022]	210.79 (-) [210.79]	0.00 (0.00) [0]

517	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA	3/2018	7/2019 (-) [0/0]	253.44 (-) [253.44]	51.77 (0.00) [0]
518	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0	3/2018	8/2018 (-) [0/0]	404.17 (-) [404.17]	163.90 (0.00) [0]
519	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM	3/2018	11/2018 (-) [0/0]	216.00 (-) [216.00]	82.85 (0.00) [0]
	<u>JHARKHAND</u>				
	<u>Coal</u>				
520	CHITRA EAST (RCE) OCP	8/2018	3/2024 (-) [3/2024]	513.98 (-) [513.98]	121.23 (0.00) [0]
521	CHURI BENTI UG (0.81 MTY)	8/2007	3/2011 (-) [3/2022]	163.51 (-) [163.51]	107.27 (0.00) [132]
522	HURA - C OC (3 MTY)	10/2015	3/2022 (-) [3/2022]	359.69 (-) [359.69]	247.51 (0.00) [0]
523	KARMA OCP (1.0MTY)	6/2009	3/2014 (-) [3/2022]	162.46 (-) [162.46]	98.21 (0.00) [96]
524	MADHUBAND NLW WASHERY	8/2010	5/2014 (-) [7/2021]	289.45 (-) [289.45]	281.33 (0.00) [86]
525	MAGADH EXPANSION OC(51 MTY)	8/2008	7/2012 (3/2025) [3/2025]	6,964.33 (6,964.33) [706.40]	706.20 (-6,257.93) [152]
526	MOONIDIH XV SEAM UG	8/2011	4/2015 (-) [3/2022]	1,230.27 (-) [1,230.27]	463.92 (0.00) [83]
527	MURAI DIH UG TURN-KEY PROJECT	2/2011	4/2014 (-) [4/2023]	339.88 (-) [339.88]	24.23 (0.00) [108]
528	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY)	2/2014	3/2021 (-) [0/0]	555.52 (-) [555.52]	5.87 (0.00) [0]
529	NORTH URIMARI EXPANSION OCP	3/2019	3/2023 (-) [3/2023]	1,553.06 (-) [1,553.06]	277.47 (0.00) [0]
530	PACHWARA SOUTH COAL BLOCK	7/2013	8/2022 (-) [9/2023]	1,795.01 (-) [1,795.01]	34.88 (0.00) [13]
531	PATHERDIH 2.5 NLW COAL WASHERY	10/2015	4/2018 (-) [6/2022]	243.00 (334.27) [334.27]	18.35 (91.27) [50]
532	PATHERDIH NLW WASHERY	10/2012	4/2014 (-) [4/2020]	269.82 (-) [269.82]	208.76 (0.00) [0]
533	RAJRAPPA RCE OCP (3.0 MTY)	12/2009	3/2016 (-) [3/2022]	510.85 (-) [510.85]	426.30 (0.00) [72]
534	RECAST EPR AMRAPALI OC	2/2012	3/2020 (3/2024) [3/2024]	4,983.58 (4,983.58) [4,983.58]	245.85 (0.00) [48]
535	TETARIAKHAR EXPANSION OCP	11/2019	3/2023 (-) [3/2023]	243.52 (-) [243.52]	39.79 (0.00) [0]
	<u>Human Resource Development</u>				
536	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT	9/2012	3/2016	171.86	111.29

	ISM DHANBAD		(-) [6/2021]	(-) [171.86]	(0.00) [63]
	<u>Petroleum</u>				
537	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE	6/2017	6/2020 (9/2021) [9/2021]	161.50 (-) [161.50]	78.18 (0.00) [15]
538	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI	10/2017	10/2022 (-) [10/2022]	226.45 (-) [226.45]	110.99 (0.00) [0]
539	CITY GAS DISTRIBUTION, JAMSHEDPUR	10/2017	10/2022 (-) [10/2022]	221.45 (-) [221.45]	92.99 (0.00) [0]
540	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	12/2015	3/2023 (3/2022) [3/2022]	823.27 (1,137.79) [1,137.79]	669.73 (314.52) [-12]
541	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO.	11/2018	6/2022 (-) [6/2022]	248.55 (-) [248.55]	109.38 (0.00) [0]
	<u>Power</u>				
542	NORTH KARANPURA STPP (3X660 MW)	2/2014	6/2019 (10/2022) [10/2022]	14,366.58 (-) [15,389.42]	11,722.10 (1,022.84) [40]
543	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017 (-) [0/0]	4,237.96 (4,238.00) [4,552.00]	3,601.54 (314.04) [0]
544	PATRATU STPP-I (3X800MW)	11/2017	3/2023 (-) [9/2024]	18,668.00 (-) [17,112.00]	4,351.86 (-1,556.00) [18]
	<u>Railways</u>				
545	BONDAMUNDA RANCHI DOUBLING	3/2016	3/2021 (3/2021) [12/2023]	1,724.20 (-) [1,724.20]	839.51 (0.00) [33]
546	GARHWA ROAD-RAMNA	3/2015	3/2021 (-) [3/2022]	348.23 (-) [348.23]	336.32 (0.00) [12]
547	KODERMA-RANCHI VIA BARKAKANA (NL),ECR	3/1999	/ (-) [3/2022]	1,033.07 (-) [3,550.00]	3,567.20 (2,516.93) [-]
548	KODERMA-TILAIYA (NL), ECR	4/2002	/ (-) [3/2023]	459.91 (-) [1,625.87]	758.44 (1,165.96) [-]
549	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	4/2012	12/2018 (12/2018) [4/2021]	258.20 (358.68) [358.68]	314.33 (100.48) [28]
550	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	4/2012	12/2016 (-) [8/2020]	148.77 (-) [377.00]	201.09 (228.23) [0]
	<u>Road Transport And Highways</u>				
551	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K	3/2018	/ (-) [0/0]	1,005.08 (-) [1,005.08]	0.00 (0.00) [0]
552	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION	2/2016	3/2019 (-) [0/0]	997.15 (-) [1,115.95]	975.08 (118.80) [0]
553	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31	1/2018	/ (-) [0/0]	273.46 (-) [276.17]	72.53 (2.71) [0]
554	FOUR LANING OF BARHI-HAZARIBAGH NH-33	8/2016	8/2018 (-) [0/0]	323.72 (-) [336.60]	312.79 (12.88) [0]
555	RANCHI-RARGA-JAMSETHPUR	12/2012	6/2015	1,479.00	740.26

			(-) [0/0]	(-) [1,479.00]	(0.00) [0]
556	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L	3/2018	6/2020 (-) [1/2021]	212.99 (-) [212.99]	156.72 (0.00) [0]
557	SIX LANEING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION	1/2018	/	1,155.16	366.61
			(-) [0/0]	(-) [1,155.16]	(0.00) [0]
558	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH-	7/2016	/	458.03	432.16
			(-) [0/0]	(-) [486.00]	(27.97) [0]
559	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I	12/2016	9/2021 (-) [9/2021]	196.00 (-) [196.00]	47.95 (0.00) [0]
	<u>Steel</u>				
560	NEW SINTER PLANT AT BOKARO STEEL PLANT	3/2015	10/2017 (12/2021) [12/2021]	1,034.01 (-) [1,034.01]	537.82 (0.00) [50]
561	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	11/2016	6/2019 (5/2021) [8/2021]	262.87 (-) [262.87]	185.85 (0.00) [26]
	<u>KARNATAKA</u>				
	<u>Defence Production</u>				
562	RESIDENTIAL QUATERS FOR HAL,BANGLORE	12/2016	2/2020 (-) [12/2021]	246.31 (-) [210.00]	131.46 (-36.31) [22]
	<u>Human Resource Development</u>				
563	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A)	7/2019	3/2022 (-) [9/2022]	851.00 (851.00) [851.00]	26.10 (0.00) [6]
	<u>Petroleum</u>				
564	BSVI UPGRADATION	9/2016	12/2019 (4/2021) [2/2022]	1,810.00 (1,810.00) [1,810.00]	1,658.31 (0.00) [26]
565	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE	12/2018	12/2022 (-) [12/2022]	854.00 (-) [854.00]	150.14 (0.00) [0]
566	DEVANGONTHI MARKETING TERMINAL	6/2020	6/2023 (-) [6/2023]	200.00 (-) [200.00]	2.26 (0.00) [0]
567	HASSAN CHERLAPALLI LPG PIPELINE	6/2019	6/2022 (-) [6/2022]	2,166.38 (-) [2,166.38]	922.06 (0.00) [0]
568	RESITEMENT OF RAICHUR DEPOT TO GULBARGA	10/2018	3/2021 (-) [5/2021]	206.26 (-) [206.26]	132.84 (0.00) [2]
569	SEA WATER DESALINATION PLANT	11/2017	3/2020 (11/2020) [7/2021]	581.00 (637.00) [637.00]	489.10 (56.00) [16]
570	SETTING UP OF PHASE LL FACILITIES FOR HPCL GREEN R AND D CENTRE AT BENGALURU	6/2018	11/2021 (-) [11/2021]	380.00 (-) [380.00]	222.20 (0.00) [0]
	<u>Power</u>				
571	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B)	5/2017	2/2019 (2/2021) [2/2021]	445.89 (675.73) [675.73]	463.08 (229.84) [0]
	<u>Railways</u>				
572	ARSIKERE-TUMKUR	3/2015	3/2020 (6/2021) [6/2021]	578.00 (-) [783.00]	620.29 (205.00) [15]
573	BAGALKOT-KUDACHI NL	4/2010	3/2016	986.30	312.23

			(-) [12/2023]	(-) [986.30]	(0.00) [93]
574	BANGLORE - SATYAMANGALAM (NL)(SWR)	4/1996	3/2002 (-) [3/2024]	1,382.78 (-) [1,382.78]	7.35 (0.00) [264]
575	CHIKBALLA-PUR-GOWRIBIDANUR NL	4/2013	/ (-) [12/2023]	327.25 (-) [327.25]	0.00 (0.00) [-]
576	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	4/2013	/ (-) [12/2023]	558.00 (-) [558.00]	0.00 (0.00) [-]
577	GADAG-WADI NL	4/2013	12/2018 (-) [6/2025]	2,841.84 (-) [2,841.84]	304.83 (0.00) [78]
578	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	4/2010	3/2023 (-) [12/2022]	2,127.00 (-) [3,000.00]	2,208.46 (873.00) [-3]
579	HUBLI- CHIKJAJUR	3/2015	3/2020 (3/2023) [3/2023]	1,156.94 (-) [1,656.00]	1,160.49 (499.06) [36]
580	HUBLI-ANKOLA(NL),SWR	4/1997	/ (-) [12/2024]	2,315.00 (-) [3,911.65]	157.01 (1,596.65) [-]
581	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	3/1996	3/2017 (3/2025) [3/2025]	644.78 (-) [998.00]	463.45 (353.22) [96]
582	MARIKUPPAM - KUPPAM	4/2012	3/2016 (-) [12/2023]	279.54 (-) [279.54]	35.29 (0.00) [93]
583	SHIMOGA-HARIHAR NL	4/2011	3/2016 (-) [3/2024]	832.47 (-) [832.47]	0.94 (0.00) [96]
584	TORANAGALLU-RANJITPURA DL	4/2011	/ (-) [12/2023]	146.75 (-) [167.50]	0.34 (20.75) [-]
585	TUMKUR-CHITRADURGA-DAVENGERE NL	4/2011	/ (-) [12/2023]	1,801.01 (-) [1,967.00]	71.56 (165.99) [-]
586	WHITE FIELD-KOLAR NL	4/2011	/ (-) [12/2023]	348.85 (-) [348.85]	0.36 (0.00) [-]
	Road Transport And Highways				
587	HOSPET-BELLARY-KARNATAKA AP BORDER	8/2016	3/2019 (1/2021) [12/2021]	1,167.42 (-) [870.00]	333.68 (-297.42) [33]
588	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM	2/2018	/ (-) [0/0]	486.78 (-) [486.78]	171.98 (0.00) [0]
589	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	5/2014	8/2016 (-) [12/2020]	1,655.01 (-) [1,655.01]	1,867.51 (0.00) [0]
590	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	3/2016	3/2019 (3/2022) [3/2022]	701.40 (-) [701.40]	132.05 (0.00) [36]
591	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL	3/2016	3/2019 (-) [11/2020]	870.00 (-) [870.00]	36.30 (0.00) [0]
592	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION	2/2017	5/2019 (-) [5/2021]	157.32 (188.00) [157.32]	0.00 (0.00) [24]
593	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE	5/2018	5/2018	171.60	0.86

	FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT		(-) [0/0]	(-) [171.60]	(0.00) [0]
594	FOUR LANING OF HOSPET - CHITRADURGA	3/2015	8/2018 (-) [0/0]	1,388.00 (-) [1,388.00]	1,295.00 (0.00) [0]
595	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB	8/2016	4/2020 (-) [12/2020]	1,664.20 (-) [1,664.20]	1,003.87 (0.00) [0]
596	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	9/2010	6/2018 (-) [0/0]	946.00 (-) [946.00]	818.53 (0.00) [0]
597	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN	3/2018	10/2018 (-) [0/0]	325.86 (-) [325.86]	326.88 (0.00) [0]
598	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH	8/2016	2/2017 (-) [0/0]	175.50 (-) [175.50]	86.54 (0.00) [0]
599	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2	3/2018	6/2019 (-) [0/0]	159.97 (-) [159.97]	0.00 (0.00) [0]
600	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM.	1/2014	8/2014 (-) [0/0]	471.16 (-) [471.16]	128.32 (0.00) [0]
601	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	1/1991	1/2018 (-) [0/0]	219.40 (-) [219.40]	0.00 (0.00) [0]
602	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O	3/2017	3/2020 (-) [0/0]	993.16 (-) [1,434.00]	1,201.43 (440.84) [0]
603	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	3/2017	3/2020 (-) [0/0]	831.58 (-) [1,177.00]	912.40 (345.42) [0]
604	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA	2/2018	/ (-) [0/0]	2,177.80 (-) [2,450.00]	2,244.98 (272.20) [0]
605	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT	2/2018	/ (-) [11/2021]	1,995.34 (-) [2,400.00]	3,088.59 (404.66) [-]
606	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP	3/2015	11/2015 (-) [0/0]	165.67 (-) [165.67]	0.00 (0.00) [0]
607	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU	3/2015	11/2015 (-) [0/0]	159.12 (-) [159.12]	0.00 (0.00) [0]
608	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	9/2016	8/2019 (-) [0/0]	950.69 (-) [1,108.00]	1,429.25 (157.31) [0]
609	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN	10/2016	3/2017 (-) [0/0]	396.96 (-) [396.96]	113.98 (0.00) [0]
610	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT	11/2016	3/2017 (-) [0/0]	314.90 (-) [314.90]	104.40 (0.00) [0]
611	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT	8/2016	1/2017 (-) [0/0]	367.44 (-) [367.44]	61.95 (0.00) [0]
612	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT	8/2016	2/2017 (-) [0/0]	329.01 (-) [329.01]	135.50 (0.00) [0]
613	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-	9/2017	10/2018 (-)	191.60 (-)	26.24 (0.00)

	HULIYAR		[0/0]	[191.60]	[0]
614	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U	1/2017	8/2017 (-) [0/0]	291.49 (-) [291.49]	130.00 (0.00) [0]
615	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA	1/2017	9/2017 (-) [0/0]	166.67 (-) [166.67]	117.05 (0.00) [0]
616	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT	8/2016	1/2017 (-) [0/0]	175.20 (-) [175.20]	113.38 (0.00) [0]
617	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH-	12/2017	1/2019 (-) [0/0]	297.30 (-) [297.30]	0.00 (0.00) [0]
618	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION	1/2018	7/2018 (-) [0/0]	159.70 (-) [159.70]	22.79 (0.00) [0]
619	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776)	3/2015	1/2016 (-) [0/0]	165.67 (-) [165.67]	87.63 (0.00) [0]
620	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775)	3/2015	1/2016 (-) [0/0]	159.12 (-) [159.12]	96.22 (0.00) [0]
	<u>Urban Development</u>				
621	BANGALORE METRO RAIL PROJECT PHASE-2	2/2014	2/2019 (3/2021) [6/2024]	26,405.14 (30,695.12) [30,695.12]	17,021.86 (4,289.98) [64]
	<u>KERALA</u>				
	<u>Health And Family Welfare</u>				
622	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST)	9/2017	3/2020 (-) [12/2021]	150.29 (-) [150.29]	43.43 (0.00) [21]
	<u>Human Resource Development</u>				
623	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE,KANJIKODE WEST, DISTRICT PALAKKA	7/2019	3/2021 (-) [6/2022]	753.63 (-) [753.63]	58.47 (0.00) [15]
624	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	1/2010	10/2012 (-) [0/0]	165.23 (-) [165.23]	118.52 (0.00) [0]
	<u>Petroleum</u>				
625	KOCHI SALEM LPG PIPELINE PROJECT	12/2015	6/2019 (-) [2/2022]	1,112.00 (1,507.24) [1,507.24]	730.00 (395.24) [32]
626	LPG TERMINAL AT KOCHI	10/2015	10/2017 (3/2022) [3/2022]	607.06 (1,236.00) [1,236.00]	394.74 (628.94) [53]
627	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY	2/2016	2/2020 (3/2021) [5/2021]	3,313.00 (-) [3,288.96]	2,967.01 (-24.04) [15]
628	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	11/2014	8/2018 (11/2019) [5/2021]	4,588.29 (5,245.96) [5,245.96]	5,076.00 (657.67) [33]
629	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC	9/2018	3/2023 (-) [3/2023]	11,130.00 (-) [11,130.00]	379.09 (0.00) [0]
	<u>Power</u>				
630	KAYAMKULAM SOLAR 70 MW	9/2019	6/2021 (10/2021) [10/2021]	403.62 (-) [403.62]	53.13 (0.00) [4]
	<u>Railways</u>				
631	ANGAMALI-SABARIMALA (N.L.)(SR)	10/1998	/ (-)	1,566.00 (-)	262.68 (1,249.62)

			[0/0]	[2,815.62]	[0]
632	ERNAKULAM-KUMBALAM	4/2010	/	189.24	6.73
			(-)	(-)	(85.97)
			[0/0]	[275.21]	[0]
633	KUMBALAM-TURAVUR	4/2011	/	252.96	8.50
			(-)	(-)	(116.59)
			[0/0]	[369.55]	[0]
634	PALAKKAD - SETTING UP OF RAIL COACH FACTORY	2/2012	3/2016	550.00	0.00
			(-)	(-)	(0.00)
			[0/0]	[550.00]	[0]
635	TRIVANDRUM-KANYAKUMARI DOUBLING	2/2015	/	1,431.90	198.81
			(-)	(-)	(0.00)
			[0/0]	[1,431.90]	[0]
636	TURAVUR-AMBALAPUZHA DOUBLING	2/2015	/	1,000.00	0.81
			(-)	(-)	(246.00)
			[0/0]	[1,246.00]	[0]
	<u>Road Transport And Highways</u>				
637	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47	6/2015	/	845.24	889.83
			(-)	(-)	(95.76)
			[1/2020]	[941.00]	[0]
638	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T	4/2016	6/2018	804.97	522.80
			(-)	(-)	(0.00)
			[3/2021]	[804.97]	[0]
639	4-LANNING OF THALSERRY -MAHE BYPASS	9/2017	9/2017	1,124.11	527.67
			(-)	(-)	(108.65)
			[5/2021]	[1,232.76]	[44]
640	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH	2/2018	/	1,424.77	14.19
			(-)	(-)	(428.65)
			[0/0]	[1,853.42]	[0]
641	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1	1/2014	9/2017	255.75	290.12
			(-)	(348.00)	(92.68)
			[0/0]	[348.43]	[0]
642	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM	2/2010	8/2012	617.00	943.17
			(-)	(-)	(0.00)
			[0/0]	[617.00]	[0]
	<u>Urban Development</u>				
643	KOCHI METRO RAIL PROJECT	7/2012	7/2017	5,181.79	6,059.17
			(-)	(-)	(1,036.35)
			[9/2020]	[6,218.14]	[0]
	<u>MADHYA PRADESH</u>				
	<u>Civil Aviation</u>				
644	UPGRADATION OF JABALPUR AIRPORT	6/2016	6/2021	412.24	195.70
			(-)	(-)	(0.00)
			[12/2021]	[412.24]	[6]
	<u>Coal</u>				
645	AMADAND OPENCASE EXPANSION PROJECT	3/2016	3/2021	869.44	123.17
			(-)	(-)	(0.00)
			[3/2022]	[869.44]	[12]
646	AMRITDHARA OC PROJECT	2/2015	3/2023	481.60	0.00
			(-)	(-)	(0.00)
			[3/2023]	[481.60]	[0]
647	BATURA HIGHWALL PROJECT	7/2015	3/2022	231.92	1.62
			(-)	(-)	(0.00)
			[3/2022]	[231.92]	[0]
648	BLOCK-B EXPANSION OPENCASE PROJECT	7/2019	3/2023	998.71	0.00
			(-)	(-)	(0.00)
			[3/2023]	[998.71]	[0]
649	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA)	11/2017	3/2022	1,255.17	152.16
			(-)	(-)	(0.00)
			[3/2023]	[1,255.17]	[12]
650	GANDHIGRAM UG MINE	8/2019	3/2026	414.16	0.87

			(-) [3/2026]	(-) [414.16]	(0.00) [0]
651	JAYANT EXPANSION OCP 10 TO 20 MTPA	5/2017	3/2021 (-) [3/2022]	1,783.09 (-) [1,783.09]	622.66 (0.00) [12]
652	KANCHAN OC EXPANSION	12/2014	3/2021 (-) [3/2024]	371.04 (-) [371.04]	77.27 (0.00) [36]
653	NIGAHI EXPANSION OCP (15 TO 25 MTPA)	11/2020	3/2025 (-) [3/2025]	1,729.68 (-) [1,729.68]	0.00 (0.00) [0]
654	RAJNAGAR OCP RPR (1.70 MTY)	12/2014	3/2021 (4/2024) [4/2024]	357.80 (-) [357.80]	100.63 (0.00) [37]
655	RPR FOR JAMUNIA UG (0.90 MTY)	7/2016	3/2022 (-) [3/2026]	281.25 (-) [281.25]	21.35 (0.00) [48]
656	SEMARIA OPENCAST PROJECT	5/2019	3/2026 (-) [3/2026]	396.58 (-) [396.58]	0.00 (0.00) [0]
657	VISHNUPURI UG TO OC MINE	7/2018	3/2025 (-) [3/2025]	195.57 (-) [195.57]	2.94 (0.00) [0]
	<u>Petroleum</u>				
658	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND	8/2017	6/2020 (9/2021) [9/2021]	236.00 (293.00) [293.00]	161.05 (57.00) [15]
	<u>Power</u>				
659	AMELIA COAL MINE	1/2017	9/2020 (8/2022) [8/2022]	2,104.21 (-) [1,587.16]	495.58 (-517.05) [23]
660	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	3/2013	1/2018 (-) [2/2021]	11,638.55 (-) [15,105.22]	13,657.43 (3,466.67) [0]
661	KHARGONE STPP STAGE I (1320 MW)	3/2015	1/2020 (-) [0/0]	9,870.51 (-) [11,148.86]	10,019.31 (1,278.35) [0]
	<u>Railways</u>				
662	ANUPPUR-KATNI	4/2015	12/2021 (-) [12/2023]	1,370.00 (-) [1,370.94]	470.49 (0.94) [24]
663	BINA - KOTA DOUBLING WITH RE	4/2011	12/2020 (-) [12/2021]	1,485.85 (-) [1,835.83]	1,571.35 (349.98) [12]
664	CHHINDWARA - NAGPUR (GC)(SECR)	4/2005	/ (-) [0/0]	383.79 (-) [1,413.76]	1,416.77 (1,029.97) [0]
665	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	4/2010	2/2019 (-) [12/2021]	585.93 (-) [1,268.32]	941.56 (682.39) [34]
666	INDORE-DEWAS-UJJAIN (80 KMS)	4/2016	6/2020 (3/2023) [3/2023]	700.00 (603.69) [603.69]	254.73 (-96.31) [33]
667	KATNI - SINGRAULI DOUBLING PROJECT	12/2015	3/2020 (-) [3/2024]	1,763.93 (-) [1,762.94]	1,156.42 (-0.99) [48]
668	KATNI GRADE SEPARATOR/BYE PASS	8/2016	3/2022 (-) [3/2023]	582.13 (1,247.64) [1,247.64]	296.69 (665.51) [12]
669	KATNI-BINA 3RD LINE (263 KM)	6/2016	3/2022 (-)	2,478.23 (-)	477.93 (0.00)

			[3/2023]	[2,478.23]	[12]
670	MULTI MODAL LOGISTICS PARK AT TIHI	12/2015	3/2019 (-) [0/0]	174.00 (-) [174.00]	172.08 (0.00) [0]
671	RAMGANJMUNDI-BHOPAL (NL),WCR	4/2001	3/2021 (3/2029) [3/2023]	424.60 (-) [2,909.99]	1,229.79 (2,485.39) [24]
672	RATLAM-MHOW-KHANDWA-AKOLA (GC)	4/2008	3/2022 (3/2024) [3/2024]	3,503.69 (5,912.40) [5,912.40]	2,161.74 (2,408.71) [24]
Road Transport And Highways					
673	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP	3/2018	11/2019 (-) [1/2021]	191.21 (-) [191.21]	127.13 (0.00) [0]
674	2L+PS OF THIKRI ANJAD SECTION OF NH-347B	11/2017	7/2018 (3/2021) [4/2021]	249.05 (-) [249.05]	195.13 (0.00) [33]
675	ANJANGAON TO MAH/MP BORDER	1/2017	6/2019 (-) [0/0]	359.00 (359.00) [359.00]	315.85 (0.00) [0]
676	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN	12/2017	/ (-) [8/2021]	950.27 (-) [950.27]	224.81 (0.00) [-]
677	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM.	11/2017	3/2018 (6/2021) [6/2021]	392.33 (428.55) [428.55]	351.92 (36.22) [39]
678	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION	8/2016	1/2019 (-) [0/0]	227.49 (-) [227.49]	195.73 (0.00) [0]
679	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12	9/2017	9/2017 (-) [0/0]	374.40 (-) [204.65]	221.79 (-169.75) [0]
680	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69	9/2017	9/2017 (-) [1/2021]	990.61 (-) [990.61]	648.40 (0.00) [0]
681	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP	8/2015	/ (-) [0/0]	257.80 (-) [257.00]	12.38 (-0.80) [0]
682	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A	6/2015	/ (3/2021) [6/2021]	390.51 (-) [390.51]	257.01 (0.00) [-]
683	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V	12/2017	/ (-) [11/2022]	656.98 (-) [840.00]	105.50 (183.02) [-]
684	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA	10/2019	/ (-) [12/2021]	743.88 (-) [743.89]	298.54 (0.01) [-]
685	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA	12/2017	/ (-) [2/2022]	1,094.97 (-) [1,094.97]	0.00 (0.00) [-]
686	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM	12/2017	/ (-) [0/0]	217.96 (-) [884.00]	257.13 (666.04) [0]
687	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH.	1/2017	3/2017 (-) [6/2021]	205.05 (-) [205.05]	123.20 (0.00) [51]
688	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD	1/2019	3/2021 (11/2021) [11/2021]	264.50 (-) [264.50]	85.70 (0.00) [8]
689	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM	1/2018	/ (-)	960.24 (-)	738.74 (0.00)

	624.480 TO		[0/0]	[960.24]	[0]
690	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA	6/2015	3/2016 (-) [0/0]	1,012.90 (-) [1,012.90]	226.10 (0.00) [0]
691	FOUR LANING OF GWALIOR-SHIVPURI	5/2013	11/2015 (-) [0/0]	1,055.00 (-) [1,601.77]	1,393.40 (546.77) [0]
692	FOUR LANING OF JABALPUR - LAKHNADON	3/2015	/ (-) [6/2015]	928.83 (-) [928.83]	824.83 (0.00) [0]
693	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I	3/2015	/ (-) [5/2020]	794.30 (679.94) [691.38]	669.35 (-102.92) [0]
694	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II	3/2015	/ (-) [5/2020]	795.76 (686.13) [686.13]	669.94 (-109.63) [0]
695	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV	3/2015	/ (6/2015) [6/2015]	810.22 (-) [810.22]	771.23 (0.00) [0]
696	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124.	10/2017	10/2017 (-) [0/0]	639.97 (-) [639.97]	473.85 (0.00) [0]
697	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER	1/2018	/ (-) [7/2018]	770.73 (-) [770.73]	350.68 (0.00) [0]
698	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93	12/2015	2/2020 (4/2021) [4/2021]	957.54 (-) [957.54]	756.69 (0.00) [14]
699	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	11/2013	5/2017 (-) [4/2021]	497.05 (-) [881.05]	754.27 (384.00) [47]
700	INDORE-DEWAS(NH-3)	11/2010	5/2013 (-) [0/0]	325.00 (-) [475.00]	469.54 (150.00) [0]
701	INDORE-JHABUA-GUJRAT/MP	10/2010	4/2013 (-) [0/0]	1,175.00 (-) [1,175.00]	1,509.96 (0.00) [0]
702	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400	11/2015	1/2020 (1/2021) [6/2021]	628.45 (-) [628.45]	439.63 (0.00) [17]
703	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP	1/2012	4/2015 (-) [3/2021]	410.72 (-) [410.72]	390.00 (0.00) [0]
704	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE	2/2019	12/2019 (-) [12/2021]	990.97 (-) [990.97]	569.29 (0.00) [24]
705	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS- CONTROLLED EXPRESSWAY FROM BAWDI VILLAG	3/2019	5/2020 (-) [5/2022]	1,047.00 (-) [1,047.00]	367.12 (0.00) [24]
706	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO	2/2019	3/2020 (-) [4/2022]	847.00 (-) [847.00]	393.93 (0.00) [25]
707	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T	2/2019	3/2020 (-) [0/0]	996.27 (-) [996.27]	419.25 (0.00) [0]
708	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA	2/2018	3/2018 (-) [6/2021]	169.63 (-) [169.63]	46.52 (0.00) [39]
709	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86	9/2016	9/2018 (-) [0/0]	178.23 (-) [178.23]	122.99 (0.00) [0]

710	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175	9/2016	1/2019 (9/2020) [11/2020]	287.34 (-) [287.34]	194.85 (0.00) [0]
711	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM	3/2016	6/2019 (4/2021) [4/2021]	877.79 (-) [877.79]	687.99 (0.00) [22]
712	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID	11/2017	2/2018 (2/2021) [2/2021]	235.91 (-) [235.91]	176.23 (0.00) [0]
713	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS	1/2016	7/2018 (5/2021) [5/2021]	809.16 (-) [809.16]	573.85 (0.00) [34]
714	SATANA-BELA SECTION OF NH-75(4L) IN MP	1/2012	8/2015 (-) [0/0]	320.48 (-) [320.48]	189.49 (0.00) [0]
715	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	11/2011	9/2015 (-) [10/2021]	954.43 (-) [1,191.51]	235.61 (237.08) [73]
716	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200	3/2015	8/2017 (6/2021) [6/2021]	511.83 (-) [511.83]	375.50 (0.00) [46]
717	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS	11/2017	2/2018 (3/2021) [6/2021]	254.17 (-) [254.17]	164.68 (0.00) [40]
718	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS	3/2018	3/2018 (-) [6/2021]	233.04 (-) [233.04]	158.22 (0.00) [39]
719	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS	2/2018	3/2018 (12/2020) [6/2021]	279.44 (-) [279.44]	156.14 (0.00) [39]
720	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS	3/2018	8/2018 (-) [0/0]	166.21 (-) [173.41]	141.65 (7.20) [0]
721	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS	11/2017	2/2018 (6/2021) [6/2021]	184.62 (-) [184.62]	86.32 (0.00) [40]
722	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS	3/2018	3/2018 (-) [9/2021]	214.69 (-) [214.69]	69.34 (0.00) [42]
723	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS	3/2018	8/2018 (9/2021) [9/2021]	217.22 (-) [226.88]	170.96 (9.66) [37]
724	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS	3/2018	3/2018 (-) [6/2021]	162.56 (-) [162.56]	129.98 (0.00) [39]
725	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A	1/2017	9/2019 (6/2021) [6/2021]	373.82 (-) [373.82]	197.04 (0.00) [21]
	<u>Urban Development</u>				
726	BHOPAL METRO RAIL	11/2018	2/2023 (-) [2/2023]	6,941.40 (-) [6,941.40]	174.53 (0.00) [0]
727	INDORE METRO RAIL	11/2018	2/2023 (-) [2/2023]	7,500.80 (-) [7,500.80]	130.21 (0.00) [0]
	<u>MAHARASHTRA</u>				
	<u>Civil Aviation</u>				
728	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT	3/2017	4/2021 (-) [4/2021]	475.39 (-) [475.39]	88.11 (0.00) [0]
	<u>Coal</u>				

729	ADASA UG TO OC	8/2015	3/2023 (-) [3/2024]	288.90 (-) [333.43]	142.27 (44.53) [12]
730	AMALGAMATED GONDEGAON GHATROHAN OC	2/2016	3/2019 (-) [3/2022]	198.68 (-) [325.18]	253.17 (126.50) [36]
731	AMALGAMATED PAUNI-II III OC MINE	6/2015	3/2021 (-) [3/2021]	483.69 (499.00) [499.00]	252.15 (15.31) [0]
732	AMALGAMATED YEKONA-I YEKONA-II	8/2015	3/2025 (-) [3/2025]	727.28 (745.03) [745.03]	365.38 (17.75) [0]
733	BELLORA-NAIGAON DEEP OC	11/2018	3/2021 (-) [9/2022]	252.71 (-) [252.71]	101.09 (0.00) [18]
734	BHANEKAON OC	2/2015	3/2023 (-) [3/2023]	187.94 (-) [409.68]	86.81 (221.74) [0]
735	BHATADI EXPANSION OC MINE	2/2016	3/2019 (-) [9/2026]	304.52 (-) [729.86]	160.67 (425.34) [90]
736	KOLAR PIMPRI EXTENSION OC	3/2017	3/2020 (-) [9/2022]	362.73 (-) [402.90]	330.34 (40.17) [30]
737	NEW MAJRI UG TO OC	5/2015	3/2019 (-) [9/2026]	295.56 (-) [496.38]	164.25 (200.82) [90]
738	PR FOR DINESH(MAKARDHOKRA III) EXPANSION OC (8.0 MTY)	11/2014	3/2020 (-) [3/2027]	1,184.33 (-) [1,184.33]	383.13 (0.00) [84]
739	REVISED PR FOR AMALGAMATED INDER KAMPTEE DEEP OC (3.2 MTY)	11/2015	3/2021 (-) [3/2024]	313.34 (-) [313.34]	148.72 (0.00) [36]
740	RPR FOR MUNGOLI NIORGUDA EXTENSION (DEEP) OC (4.375 MTY)	11/2015	3/2020 (-) [3/2026]	851.60 (-) [826.80]	230.50 (-24.80) [72]
741	SINGHORI OC MINE	6/2015	3/2020 (-) [9/2021]	205.49 (-) [205.49]	138.12 (0.00) [18]
742	UKNI DEEP OC	11/2018	3/2021 (-) [9/2022]	318.14 (-) [318.14]	211.41 (0.00) [18]
	Fertilisers				
743	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY	4/2018	4/2020 (3/2021) [7/2021]	426.72 (-) [426.72]	288.80 (0.00) [15]
	Health And Family Welfare				
744	HOSPITAL AND TEACHING- AIIMS NAGPUR	3/2018	/ (-) [6/2021]	582.99 (-) [582.99]	482.32 (0.00) [-]
745	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA	8/2017	3/2019 (-) [1/2021]	274.19 (-) [274.19]	256.37 (0.00) [0]
	Human Resource Development				
746	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI	1/2018	7/2020 (-) [6/2021]	223.37 (-) [223.37]	61.35 (0.00) [11]
	Petroleum				
747	180 TMTPA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA	6/2017	6/2020 (12/2021) [9/2021]	249.26 (-) [249.26]	134.44 (0.00) [15]

748	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [9/2021]	261.00 (-) [261.00]	158.24 (0.00) [8]
749	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [9/2021]	212.00 (-) [212.00]	148.29 (0.00) [8]
750	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [10/2021]	348.00 (-) [348.00]	217.55 (0.00) [9]
751	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	3/2011	5/2013 (2/2022) [2/2022]	861.79 (1,846.46) [2,001.00]	1,551.48 (1,139.21) [105]
752	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION	2/2019	5/2021 (12/2021) [12/2021]	2,292.46 (-) [2,203.71]	1,757.87 (-88.75) [7]
753	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)	2/2017	5/2021 (5/2021) [5/2021]	4,006.83 (4,475.92) [3,596.00]	3,514.02 (-410.83) [0]
754	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY	7/2020	12/2021 (-) [12/2021]	640.00 (-) [640.00]	326.57 (0.00) [0]
755	HEERA REDEVELOPMENT - PHASE III	6/2019	3/2022 (-) [3/2022]	2,494.68 (-) [2,354.72]	1,421.11 (-139.96) [0]
756	KEROSENE HYDROTREATER (KHT) UNIT INTEGRATED WITH EXISTING DIESEL HYDROTREATER (DHT) UNIT AT MUMBAI R	8/2020	3/2023 (-) [3/2023]	697.00 (-) [697.00]	155.18 (0.00) [0]
757	KOYALI AHMEDNAGAR SOLAPUR PIPELINE	5/2016	2/2022 (-) [2/2022]	1,945.00 (-) [1,945.00]	1,536.61 (0.00) [0]
758	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	12/2015	4/2018 (5/2022) [5/2022]	3,190.69 (3,375.90) [3,375.90]	2,786.78 (185.21) [49]
759	MMPL PIPELINE REROUTING PROJECT	4/2013	12/2019 (4/2021) [4/2021]	449.58 (-) [449.58]	396.13 (0.00) [16]
760	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	4/2019	3/2022 (5/2023) [5/2023]	3,228.80 (3,976.67) [3,976.67]	1,188.33 (747.87) [14]
761	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV	5/2019	5/2021 (1/2022) [1/2022]	3,660.71 (3,740.05) [3,740.05]	2,808.52 (79.34) [8]
762	MUMBAI REFINERY EXPANSION PROJECT	9/2015	3/2020 (-) [0/0]	4,199.00 (5,060.00) [5,060.00]	4,528.82 (861.00) [0]
763	PIPELINE REPLACEMENT PROJECT (PRP-VI)	5/2019	12/2020 (5/2021) [5/2021]	763.92 (-) [733.86]	757.62 (-30.06) [5]
764	PUNE POL STORAGE DEPOT	8/2016	8/2020 (-) [3/2021]	282.64 (-) [282.64]	246.11 (0.00) [0]
<u>Power</u>					
765	MOUDA STPP STAGE 2	3/2012	9/2016 (-) [0/0]	7,921.47 (-) [7,921.47]	5,302.00 (0.00) [0]
<u>Railways</u>					
766	3RD LINE BETWEEN BHUSAWAL-JALGAON	4/2011	3/2019 (-) [0/0]	184.06 (-) [315.00]	312.62 (130.94) [0]
767	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	2/1997	3/2021 (-)	2,271.50 (-)	2,648.51 (2,245.99)

			[3/2023]	[4,517.49]	[24]
768	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	3/1996	3/2004 (-) [3/2022]	495.44 (-) [2,980.41]	1,768.25 (2,484.97) [216]
769	DAUND - MANMAD (236 KM)	2/2016	3/2023 (-) [3/2023]	1,876.00 (-) [2,081.27]	445.15 (205.27) [0]
770	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	3/2009	3/2020 (-) [12/2021]	713.48 (-) [2,725.00]	2,554.71 (2,011.52) [21]
771	DIGHI PORT NEW LINE	4/2015	12/2025 (-) [3/2025]	723.78 (-) [723.78]	0.19 (0.00) [-9]
772	INDORE - MANMAD VIA MALEGAON (368 KM)	2/2016	3/2024 (-) [3/2024]	9,968.00 (-) [9,968.00]	0.00 (0.00) [0]
773	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	2/2015	3/2023 (-) [3/2024]	2,449.91 (-) [2,449.91]	332.19 (0.00) [12]
774	KALYAN-KASARA 3RD LINE	4/2011	3/2021 (-) [3/2023]	792.89 (-) [1,377.48]	335.23 (584.59) [24]
775	MANMAD - JALGAON - 3RD LINE (160 KM)	2/2016	3/2022 (-) [3/2024]	1,035.16 (-) [1,035.16]	244.12 (0.00) [24]
776	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN	10/2013	3/2019 (-) [12/2020]	305.00 (-) [305.00]	269.73 (0.00) [0]
777	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM	3/2010	/ (-) [0/0]	265.88 (-) [265.88]	0.00 (0.00) [0]
778	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	4/2008	3/2014 (-) [0/0]	5,300.00 (-) [918.53]	284.75 (-4,381.47) [0]
779	PUNE-MIRAJ-LONDA (467 KM)	2/2015	3/2024 (-) [3/2023]	3,627.47 (3,627.00) [3,627.47]	1,204.21 (0.00) [-12]
780	PUNE-NASIK (265 KM)	2/2016	3/2024 (-) [3/2024]	2,425.00 (-) [5,341.68]	0.00 (2,916.68) [0]
781	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	9/2016	3/2023 (-) [12/2023]	1,908.51 (-) [3,524.81]	982.38 (1,616.30) [9]
782	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE	4/2012	4/2016 (-) [0/0]	714.10 (-) [714.10]	65.20 (0.00) [0]
783	VAIBHAVWADI -KOLHAPUR (107 KM)	2/2016	3/2024 (-) [3/2024]	2,750.00 (-) [3,438.51]	0.00 (688.51) [0]
784	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A	3/2012	/ (-) [0/0]	217.38 (-) [217.38]	0.00 (0.00) [0]
785	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	6/2018	12/2021 (-) [12/2024]	229.00 (-) [1,096.00]	39.79 (867.00) [36]
786	WARDHA - NAGPUR - 4TH LINE (76 KM)	2/2016	3/2023 (-) [3/2024]	637.95 (-) [637.95]	182.65 (0.00) [12]
787	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	2/2015	3/2022 (-) [3/2023]	1,272.19 (-) [1,283.49]	408.70 (11.30) [12]

788	WARDHA-NANDED MAHARASHTRA	4/2008	3/2023 (-) [3/2023]	3,168.29 (-) [3,168.29]	1,352.27 (0.00) [0]
789	WARDHA-SEWAGRAM NGP 3RD LINE	4/2012	3/2022 (-) [3/2024]	540.02 (-) [540.02]	272.55 (0.00) [24]
	Road Transport And Highways				
790	4 LANING OF AMRAVATI - CHIKHLI (PKG-I)	7/2015	5/2019 (-) [0/0]	2,288.18 (-) [2,288.18]	487.81 (0.00) [0]
791	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3)	7/2015	5/2019 (-) [0/0]	1,885.74 (-) [1,885.74]	1,636.02 (0.00) [0]
792	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	1/2015	7/2017 (-) [0/0]	972.50 (-) [972.50]	1,492.00 (0.00) [0]
793	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104)	1/2018	/ (-) [8/2021]	607.00 (-) [607.00]	440.92 (0.00) [-]
794	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000)	1/2018	/ (-) [4/2021]	621.00 (-) [621.00]	591.21 (0.00) [-]
795	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION	6/2014	11/2016 (-) [0/0]	923.04 (-) [923.04]	861.99 (0.00) [0]
796	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	3/2017	3/2020 (-) [0/0]	744.64 (-) [982.00]	0.00 (237.36) [0]
797	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700)	11/2016	/ (-) [7/2021]	1,071.61 (-) [1,048.10]	965.72 (-23.51) [-]
798	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT	11/2016	3/2019 (-) [3/2021]	446.17 (-) [446.17]	70.85 (0.00) [0]
799	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575)	3/2017	3/2020 (-) [0/0]	1,098.06 (-) [1,160.64]	1,068.76 (62.58) [0]
800	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE	3/2016	/ (-) [0/0]	1,142.62 (-) [1,142.62]	585.85 (0.00) [0]
801	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE	3/2016	/ (-) [0/0]	1,101.58 (-) [1,101.58]	324.00 (0.00) [0]
802	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI	11/2016	3/2019 (-) [2/2021]	400.25 (-) [400.25]	105.20 (0.00) [0]
803	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00)	11/2016	/ (1/2022) [7/2021]	1,064.88 (-) [1,021.00]	336.32 (-43.88) [-]
804	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580)	3/2017	3/2017 (-) [0/0]	1,059.73 (-) [1,071.00]	610.87 (11.27) [0]
805	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690)	3/2017	3/2020 (-) [0/0]	1,030.44 (-) [1,065.51]	1,015.76 (35.07) [0]
806	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500)	3/2017	3/2020 (-) [0/0]	988.34 (-) [1,043.28]	1,035.00 (54.94) [0]
807	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3	8/2015	5/2018 (4/2019) [6/2021]	505.00 (-) [504.00]	385.08 (-1.00) [37]

808	AHMADPUR TO PIMPLA	1/2017	8/2019 (-) [0/0]	422.38 (-) [422.38]	218.78 (0.00) [0]
809	AHMEDNAGAR TO BARAMATI	1/2017	8/2019 (-) [0/0]	955.40 (-) [955.40]	446.67 (0.00) [0]
810	AKKALKOT TO DHUDHNI	4/2016	2/2019 (-) [0/0]	211.42 (-) [211.42]	131.85 (0.00) [0]
811	AKOLA TO AKOT	1/2017	6/2019 (-) [0/0]	313.95 (-) [313.95]	49.38 (0.00) [0]
812	AKOT TO ANJANGAON	1/2017	6/2019 (-) [0/0]	245.77 (246.00) [245.77]	197.90 (0.00) [0]
813	AMDNI TO SAONER	1/2017	6/2019 (-) [0/0]	396.91 (397.00) [396.91]	280.56 (0.00) [0]
814	ARDHAPUR TO HIMAYATNAGAR	12/2017	6/2020 (-) [0/0]	426.06 (426.00) [426.06]	163.86 (0.00) [0]
815	ARNI TO NAIGAINBANDI	12/2017	12/2019 (-) [0/0]	309.94 (310.00) [309.94]	173.78 (0.00) [0]
816	AURANGABAD TO SILLOD	2/2017	6/2019 (-) [0/0]	456.32 (-) [456.32]	289.08 (0.00) [0]
817	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62	3/2016	7/2018 (-) [0/0]	197.69 (-) [197.69]	151.11 (0.00) [0]
818	BAMNI TO NAVAEGAON	9/2017	4/2020 (-) [0/0]	241.69 (242.00) [241.69]	149.29 (0.00) [0]
819	BARASGAON TO RAHATEE	7/2016	9/2018 (-) [4/2021]	289.11 (290.00) [289.11]	101.90 (0.00) [31]
820	BHADGAON TO CHALISGAON	1/2018	11/2019 (-) [0/0]	259.55 (260.00) [259.55]	202.34 (0.00) [0]
821	BHANDARA TO GHOTITOK	1/2017	6/2019 (-) [0/0]	392.83 (393.00) [392.83]	273.42 (0.00) [0]
822	BHOGAN KHURD TO KASHEDI	9/2017	6/2021 (-) [6/2021]	743.21 (743.00) [743.21]	193.08 (0.00) [0]
823	BHOKAR TO SARSAM	2/2017	7/2019 (-) [0/0]	295.09 (-) [295.99]	169.64 (0.90) [0]
824	BODHWAD TO STATE BORDER	1/2017	7/2019 (-) [0/0]	178.26 (-) [178.26]	124.95 (0.00) [0]
825	CHALISGAON TO NANDGAON	3/2018	12/2019 (-) [0/0]	206.97 (207.00) [206.97]	135.41 (0.00) [0]
826	CHIKALI TO DHAD	3/2018	12/2019 (-) [0/0]	189.46 (189.00) [189.46]	97.66 (0.00) [0]
827	CHIKALI TO KHAMGAON	2/2017	6/2019 (-) [0/0]	548.03 (548.00) [548.03]	359.14 (0.00) [0]
828	CHIKLI TO TAKARKHED	3/2018	12/2019	393.10	224.68

			(-) [0/0]	(393.00) [393.10]	(0.00) [0]
829	CHIMUR TO WARORA	11/2016	3/2019 (-) [0/0]	467.70 (-) [467.70]	164.90 (0.00) [0]
830	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF	3/2018	/ (-) [7/2021]	1,162.92 (-) [1,162.92]	58.20 (0.00) [-]
831	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	12/2015	3/2019 (12/2021) [3/2022]	649.50 (-) [649.50]	209.18 (0.00) [36]
832	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6)	3/2018	/ (8/2021) [2/2022]	291.53 (-) [291.53]	150.06 (0.00) [-]
833	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST	1/2017	5/2019 (-) [0/0]	244.90 (-) [244.90]	251.87 (0.00) [0]
834	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6)	3/2018	/ (2/2021) [8/2021]	289.21 (-) [289.21]	194.57 (0.00) [-]
835	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	10/2015	5/2018 (6/2021) [6/2021]	593.26 (-) [690.17]	595.33 (96.91) [37]
836	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION	12/2011	/ (-) [0/0]	156.26 (227.00) [247.95]	175.00 (91.69) [0]
837	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	10/2015	5/2018 (6/2021) [6/2021]	531.13 (-) [730.97]	653.06 (199.84) [37]
838	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16)	3/2015	/ (-) [0/0]	168.30 (-) [168.30]	80.00 (0.00) [0]
839	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO	8/2014	7/2016 (-) [0/0]	187.79 (-) [187.79]	76.62 (0.00) [0]
840	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST	3/2017	3/2020 (-) [0/0]	247.02 (-) [157.49]	31.97 (-89.53) [0]
841	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D	9/2015	5/2018 (11/2020) [11/2020]	414.51 (-) [414.00]	409.16 (-0.51) [0]
842	DAHEGAON TO KUHI	1/2017	6/2019 (-) [0/0]	228.89 (229.00) [228.89]	154.69 (0.00) [0]
843	DASTAPUR TO KARANJA	3/2018	12/2019 (-) [0/0]	182.63 (-) [182.63]	132.40 (0.00) [0]
844	DEORI TO AMGAON	1/2017	5/2019 (-) [0/0]	409.62 (410.00) [409.62]	227.76 (0.00) [0]
845	DEULGAON SAKARSHA TO MEHKAR	3/2018	12/2019 (-) [0/0]	219.91 (-) [219.91]	123.76 (0.00) [0]
846	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000)	3/2017	3/2020 (-) [0/0]	296.19 (-) [254.00]	254.85 (-42.19) [0]
847	DHAD BHOKARDAN TO BHOKARDHAN SILLOD	3/2018	12/2019 (-) [0/0]	336.21 (336.00) [336.21]	166.82 (0.00) [0]
848	DHANGIPIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK	3/2018	2/2020 (-)	217.14 (217.00)	131.55 (0.00)

			[0/0]	[217.14]	[0]
849	DIGRAS DARWAH KARANJA	1/2017	6/2019 (-) [0/0]	391.06 (391.00) [391.06]	220.42 (0.00) [0]
850	FARDAPUR TO JALGAON	2/2017	6/2019 (-) [0/0]	456.45 (-) [456.45]	165.74 (0.00) [0]
851	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS	4/2010	6/2012 (-) [0/0]	1,170.52 (-) [1,170.52]	2,051.36 (0.00) [0]
852	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4	3/2018	/ (-) [0/0]	642.13 (-) [807.00]	666.56 (164.87) [0]
853	FOUR LANING OF AURANGABAD - YEDISHI	7/2015	1/2018 (-) [0/0]	1,871.34 (-) [1,871.34]	3,443.43 (0.00) [0]
854	FOUR LANNING OF TULJAPUR-AUSA SECTION	2/2017	2/2020 (-) [0/0]	904.16 (-) [904.16]	855.25 (0.00) [0]
855	GADCHIROLI TO MUL	12/2016	6/2019 (-) [0/0]	484.15 (-) [484.15]	309.38 (0.00) [0]
856	HELWAK TO KARAD	2/2017	7/2019 (-) [0/0]	416.99 (-) [416.99]	208.63 (0.00) [0]
857	HIMAYATNAGAR TO PHULSAWANGI	3/2018	12/2019 (-) [0/0]	294.87 (295.00) [294.87]	96.59 (0.00) [0]
858	INDAPUR TO AGARDANDA	1/2017	7/2019 (-) [0/0]	355.17 (-) [355.17]	269.58 (0.00) [0]
859	INDAPUR TO VADPALE	1/2017	12/2019 (-) [0/0]	1,202.52 (1,203.00) [1,202.52]	973.05 (0.00) [0]
860	JAHIRABAD TO LATUR	1/2017	11/2019 (-) [0/0]	461.96 (-) [461.96]	250.79 (0.00) [0]
861	JALGAON TO BHADGAON	1/2018	11/2019 (-) [0/0]	307.54 (308.00) [307.54]	198.65 (0.00) [0]
862	JALGAON TO NANDURA	3/2018	12/2019 (-) [0/0]	177.84 (177.00) [177.84]	110.20 (0.00) [0]
863	JALKOT TO TOGRI	7/2018	8/2020 (-) [0/0]	299.92 (300.00) [299.92]	51.25 (0.00) [0]
864	JINTUR TO PARBHANI	1/2017	/ (-) [0/0]	356.66 (-) [356.66]	106.68 (0.00) [0]
865	KAIJ TO KUSALAM	1/2017	7/2019 (-) [0/0]	554.78 (-) [554.78]	252.45 (0.00) [0]
866	KALMAB TO RALEGAON	1/2017	6/2019 (-) [0/0]	467.78 (-) [467.78]	317.91 (0.00) [0]
867	KALMATH TO ZARAP	9/2016	3/2020 (-) [0/0]	1,338.13 (1,338.00) [1,338.13]	1,346.39 (0.00) [0]
868	KANTE TO WAKED	3/2016	11/2019 (-) [0/0]	1,230.02 (1,230.00) [1,230.02]	627.51 (0.00) [0]

869	KARAD PATAN CHIPLUN GUHAGAR	2/2017	6/2019 (-) [0/0]	407.19 (407.00) [407.19]	108.68 (0.00) [0]
870	KARAD TO TAGAON	1/2017	6/2019 (-) [0/0]	537.81 (538.00) [537.81]	159.65 (0.00) [0]
871	KARAD TO VITA	1/2018	12/2019 (-) [0/0]	344.85 (245.00) [344.85]	190.22 (0.00) [0]
872	KARWANDI TO RAJURI	3/2018	12/2019 (-) [0/0]	276.95 (277.00) [276.95]	253.47 (0.00) [0]
873	KATOL TO WARUD	1/2017	6/2019 (-) [0/0]	463.62 (664.00) [463.62]	253.23 (0.00) [0]
874	KHAMGAON TO DEULGAON SAKARSHA	3/2018	12/2019 (-) [0/0]	249.29 (-) [249.29]	155.48 (0.00) [0]
875	KHAMGAON TO SHEGAON	2/2017	5/2019 (-) [0/0]	203.21 (203.00) [203.21]	150.09 (0.00) [0]
876	KHERDA TO NAGZARI	3/2018	12/2019 (-) [0/0]	181.30 (-) [181.30]	138.50 (0.00) [0]
877	KOLDE TO KHETIYA	1/2017	7/2019 (-) [0/0]	509.18 (-) [509.18]	228.82 (0.00) [0]
878	KOLHA TO NASRATPUR	4/2016	4/2019 (-) [0/0]	281.78 (282.00) [281.78]	281.73 (0.00) [0]
879	KOTHARI TO DHANORA	9/2018	8/2020 (-) [0/0]	301.38 (301.00) [301.38]	134.51 (0.00) [0]
880	KUMBHARI PHTA TO DEULGAON RAJA	2/2017	6/2019 (-) [0/0]	406.51 (-) [406.51]	290.69 (0.00) [0]
881	KUNDRAL TO WAZAR	1/2018	12/2019 (-) [0/0]	225.25 (225.00) [225.25]	199.34 (0.00) [0]
882	KURUDWADI TO PANDHARPUR	1/2017	7/2019 (-) [0/0]	307.63 (-) [307.63]	190.69 (0.00) [0]
883	KUSUMBA TO MALEGAON	3/2018	12/2019 (-) [0/0]	243.45 (244.00) [243.45]	146.88 (0.00) [0]
884	LATUR TO PANGAON	3/2018	12/2019 (-) [0/0]	336.47 (336.00) [336.47]	394.00 (0.00) [0]
885	MAHAD TO RAIGAD FORT	7/2018	5/2020 (-) [0/0]	237.40 (-) [237.40]	9.66 (0.00) [0]
886	MAJALGAON TO KAIJ	1/2017	7/2019 (-) [0/0]	413.99 (-) [413.99]	299.72 (0.00) [0]
887	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER	3/2018	12/2019 (-) [0/0]	256.15 (-) [256.15]	262.63 (0.00) [0]
888	MALEGAON TO RISOD	2/2018	12/2019 (-) [0/0]	303.24 (303.00) [303.24]	193.15 (0.00) [0]
889	MALEWADA TO CHIMUR	10/2016	6/2019	322.55	189.60

			(-) [0/0]	(-) [322.55]	(0.00) [0]
890	MANGAON TO DIGHI PORT	1/2017	7/2019 (-) [0/0]	457.52 (-) [457.52]	352.94 (0.00) [0]
891	MANGRUPHIR TO MAHAN	3/2018	11/2019 (-) [0/0]	222.13 (222.00) [222.13]	153.84 (0.00) [0]
892	MANJUSUMBA TO CHUMBALI	1/2017	8/2019 (-) [0/0]	228.54 (-) [228.54]	162.30 (0.00) [0]
893	MANSAR TO SALAIKHURD	1/2018	12/2019 (-) [0/0]	418.36 (-) [418.36]	263.13 (0.00) [0]
894	MANTHA TALUKAS BORDER TO PARTUR	1/2017	7/2019 (-) [0/0]	486.19 (-) [486.19]	293.39 (0.00) [0]
895	MEHKAR TO AJISPUR	1/2017	7/2019 (-) [0/0]	232.77 (-) [232.77]	148.53 (0.00) [0]
896	MEHKAR TO CHIKALI	2/2017	5/2019 (-) [0/0]	322.48 (322.00) [322.48]	229.08 (0.00) [0]
897	MHASWAD TO TEMBHURNI	1/2017	7/2019 (-) [0/0]	488.60 (-) [488.60]	223.28 (0.00) [0]
898	MORSHI TO ACHALPUR	1/2017	6/2019 (-) [0/0]	341.16 (341.00) [341.16]	228.07 (0.00) [0]
899	MORSHI TO MAH/MP BORDER	1/2017	6/2019 (-) [0/0]	471.61 (472.00) [471.61]	321.02 (0.00) [0]
900	MUL TO CHANDRAPUR	12/2016	7/2019 (-) [0/0]	162.34 (-) [162.34]	53.94 (0.00) [0]
901	NAGAJ TO VAJAPUR	1/2017	6/2019 (-) [0/0]	376.72 (377.00) [376.72]	224.81 (0.00) [0]
902	NAGBHID TO ARMORI	9/2016	7/2019 (-) [0/0]	269.05 (-) [269.05]	222.60 (0.00) [0]
903	NAGPUR RING ROAD PACKAGE-1	3/2016	7/2019 (6/2021) [12/2021]	546.00 (-) [546.00]	307.08 (0.00) [29]
904	NAGPUR RING ROAD PACKAGE-2	3/2016	7/2019 (6/2021) [12/2021]	591.66 (-) [591.66]	318.30 (0.00) [29]
905	NAIGAONBANDI TO MANGRULPIR	12/2017	3/2019 (-) [0/0]	244.04 (244.00) [244.04]	142.76 (0.00) [0]
906	NALDURG TO AKKALKOT	2/2018	12/2019 (-) [0/0]	274.50 (275.00) [274.50]	143.39 (0.00) [0]
907	NANDED TO JALKOT	12/2017	9/2019 (-) [0/0]	456.93 (457.00) [456.93]	456.93 (0.00) [0]
908	NANDGAON TO MORSHI	1/2017	6/2019 (-) [0/0]	385.87 (386.00) [385.87]	258.29 (0.00) [0]
909	NASHIK TO PETH	12/2015	11/2018 (-)	289.60 (-)	210.10 (0.00)

			[0/0]	[289.60]	[0]
910	NASRATPUR TO BARASGAON	7/2016	9/2019 (-) [0/0]	406.54 (407.00) [406.54]	163.35 (0.00) [0]
911	NILAJPHATA TO BHANDARA	1/2018	5/2020 (-) [0/0]	420.63 (421.00) [420.63]	136.88 (0.00) [0]
912	OMREGA TO AUSA	3/2018	12/2019 (-) [0/0]	272.04 (272.00) [272.04]	218.03 (0.00) [0]
913	OSMANNAGAR TO KUNDRAL	9/2017	8/2020 (-) [0/0]	344.25 (344.00) [344.25]	128.89 (0.00) [0]
914	PAHUR TO BODHWAD	1/2017	5/2020 (-) [0/0]	244.93 (-) [244.93]	127.80 (0.00) [0]
915	PAITHAN TO SHIRUR	3/2017	6/2019 (-) [0/0]	341.80 (-) [341.80]	122.32 (0.00) [0]
916	PALPHATA TO PHULAMBAR	3/2018	12/2019 (-) [0/0]	227.19 (227.00) [227.19]	125.23 (0.00) [0]
917	PANCHARAL TO MANDANGHAR	7/2018	5/2020 (-) [0/0]	381.08 (302.00) [381.08]	9.66 (0.00) [0]
918	PANDHARPUR TO SANGOLA	7/2017	7/2019 (-) [0/0]	218.38 (-) [218.38]	168.75 (0.00) [0]
919	PARBHANI TO GANGKHED	3/2018	12/2019 (-) [0/0]	238.19 (238.00) [238.19]	139.93 (0.00) [0]
920	PARLI PIMPLA DAHIGUDA	2/2017	6/2019 (-) [0/0]	205.72 (206.00) [205.72]	41.48 (0.00) [0]
921	PARSHURAM GHAT TO ARAWALI	4/2016	12/2019 (-) [0/0]	983.14 (983.00) [983.14]	709.06 (0.00) [0]
922	PARTUR TO MAJALGAON	1/2017	7/2019 (-) [0/0]	420.57 (-) [420.57]	254.22 (0.00) [0]
923	PATGAON KHOPOLI SECTION I	1/2018	12/2019 (-) [0/0]	170.00 (-) [170.00]	104.11 (0.00) [0]
924	PEN TO KHOPOLI	3/2018	3/2018 (-) [0/0]	301.39 (302.00) [301.39]	50.71 (0.00) [0]
925	PIMPLA TO MANJARSUMBHA	1/2017	8/2019 (-) [0/0]	595.77 (-) [595.77]	264.93 (0.00) [0]
926	PUNE RAIGARH DISTRICT BORDER TO MANGAON	3/2018	12/2019 (-) [0/0]	223.46 (-) [223.46]	21.42 (0.00) [0]
927	PUNE TO MALE VILLAGE	3/2018	12/2019 (-) [0/0]	228.31 (-) [228.31]	54.77 (0.00) [0]
928	PUNE-SATARA(NH-4)	10/2010	3/2013 (-) [3/2021]	1,724.55 (-) [1,724.55]	2,559.00 (0.00) [0]
929	RALEGAON TO RAMTIRTH	1/2017	7/2019 (-) [0/0]	210.81 (-) [210.81]	128.94 (0.00) [0]

930	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00	1/2014	/ (-) [0/0]	446.77 (-) [446.77]	300.50 (0.00) [0]
931	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM	1/2015	/ (-) [0/0]	225.81 (-) [225.81]	89.93 (0.00) [0]
932	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA	3/2016	12/2019 (6/2021) [6/2021]	536.65 (356.00) [536.65]	539.35 (0.00) [18]
933	RISOD TO HINGOLI	2/2018	12/2019 (-) [0/0]	355.99 (-) [355.99]	238.22 (0.00) [0]
934	SAKOLI TO BHANDARA	1/2017	6/2019 (-) [0/0]	362.96 (-) [362.96]	87.90 (0.00) [0]
935	SALAIKHURD TO TIRORA	1/2018	12/2019 (-) [0/0]	415.25 (415.25) [415.25]	220.90 (0.00) [0]
936	SANGOLA TO JATH	1/2018	12/2019 (-) [0/0]	257.38 (257.00) [257.38]	96.26 (0.00) [0]
937	SARAD VANI PIMPALGAON	1/2017	7/2019 (-) [0/0]	250.46 (-) [250.46]	137.63 (0.00) [0]
938	SARSAM TO KOTHARI	2/2016	7/2019 (-) [0/0]	545.64 (-) [545.64]	166.29 (0.00) [0]
939	SATARA MURVAD PILLOV PANDHARPUR	1/2017	/ (-) [0/0]	388.44 (-) [388.44]	187.77 (0.00) [0]
940	SATARA TO MHASWAD	1/2017	7/2019 (-) [0/0]	653.46 (-) [653.46]	252.00 (0.00) [0]
941	SELDOH TO PANVAR	7/2018	5/2020 (-) [0/0]	404.33 (404.00) [404.33]	22.40 (0.00) [0]
942	SHAHPUR PATGAON SECTION I	1/2018	12/2019 (-) [0/0]	150.79 (-) [150.79]	58.79 (0.00) [0]
943	SHEGAON TO DEORI PHATA	2/2017	5/2019 (-) [0/0]	373.10 (373.00) [373.10]	311.65 (0.00) [0]
944	SHIROD SHAHPURER TO NANDED	1/2017	7/2019 (-) [0/0]	211.34 (-) [211.34]	127.67 (0.00) [0]
945	SHIRUR TO KHARDA	2/2017	6/2019 (-) [0/0]	381.77 (-) [381.77]	177.79 (0.00) [0]
946	SHIVUR TO YEOLA	3/2018	12/2019 (-) [0/0]	181.08 (-) [181.08]	97.86 (0.00) [0]
947	SILLOD TO FARDAPUR	2/2017	6/2019 (-) [0/0]	337.46 (-) [337.46]	94.22 (0.00) [0]
948	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH	12/2017	/ (-) [10/2020]	404.94 (-) [448.18]	427.22 (43.24) [0]
949	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE	11/2016	/ (-) [0/0]	290.73 (-) [315.00]	246.70 (24.27) [0]
950	TAKARKHED TO JALNA	9/2017	6/2019	417.90	199.01

			(-) [0/0]	(418.00) [417.90]	(0.00) [0]
951	TALEGAON TO GONAPUR	1/2018	3/2019 (-) [0/0]	264.41 (264.00) [264.41]	165.67 (0.00) [0]
952	TALGAON TO KALMATH	10/2016	3/2020 (-) [0/0]	904.70 (905.00) [904.70]	969.90 (0.00) [0]
953	TASGAON TO SHIRDHON	1/2017	11/2019 (-) [0/0]	195.64 (196.00) [195.64]	116.30 (0.00) [0]
954	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI	2/2017	7/2019 (-) [0/0]	422.02 (422.00) [422.02]	278.82 (0.00) [0]
955	VADPALE TO BHOGAN KHURD	1/2017	11/2019 (-) [0/0]	1,598.47 (1,560.00) [1,598.47]	1,020.24 (0.00) [0]
956	VITA TO NAGAJ	3/2018	12/2019 (-) [0/0]	304.58 (305.00) [304.58]	97.71 (0.00) [0]
957	WADI TO ASOLA	1/2017	9/2019 (-) [0/0]	363.82 (364.00) [363.82]	39.31 (0.00) [0]
958	WADIGODRI TO DHANGRIPIMPRI	3/2018	2/2020 (-) [0/0]	194.23 (194.00) [194.23]	106.23 (0.00) [0]
959	WAKAN PALI KHOPOLI	1/2017	5/2019 (-) [0/0]	376.19 (-) [376.19]	55.87 (0.00) [0]
960	WAKED TO TALEGAON	2/2016	2/2019 (-) [0/0]	1,244.75 (1,245.00) [1,244.75]	837.21 (0.00) [0]
961	WARDHA TO ARVI	2/2018	4/2020 (-) [0/0]	313.58 (-) [313.58]	127.86 (0.00) [0]
962	WARDHA TO HINGAGHAT	1/2018	12/2019 (-) [0/0]	216.90 (217.00) [216.90]	136.45 (0.00) [0]
963	WASHIM TO DASTAPUR	3/2018	12/2019 (-) [0/0]	165.51 (-) [165.51]	127.54 (0.00) [0]
964	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16	10/2015	/ (-) [0/0]	289.60 (-) [289.60]	90.65 (0.00) [0]
965	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	5/2013	2/2014 (-) [0/0]	1,348.20 (-) [1,348.20]	1,792.90 (0.00) [0]
	<u>Urban Development</u>				
966	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	7/2013	1/2015 (-) [3/2023]	23,136.00 (-) [33,406.00]	17,039.36 (10,270.00) [98]
967	NAGPUR METRO RAIL	8/2014	3/2018 (-) [0/0]	8,680.00 (-) [8,680.00]	7,068.52 (0.00) [0]
968	PUNE METRO RAIL PROJECT (PHASE 1)	12/2016	11/2021 (-) [11/2021]	11,420.00 (11,420.00) [11,420.00]	6,214.58 (0.00) [0]
	<u>Water Resources</u>				
969	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA	3/2017	12/2019 (-) [12/2021]	233.57 (-) [233.57]	173.71 (0.00) [24]

	MANIPUR				
	Power				
970	LOKTAK D/S HEP(NHPC)	12/1999	6/2006 (-) [0/0]	578.62 (-) [578.62]	0.00 (0.00) [0]
	Railways				
971	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (-) [12/2023]	4,454.17 (-) [12,264.15]	10,994.55 (7,809.98) [153]
	Road Transport And Highways				
972	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A)	3/2020	6/2022 (-) [6/2022]	292.24 (-) [292.24]	1.74 (0.00) [0]
973	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B)	6/2020	8/2022 (-) [8/2022]	365.53 (-) [365.53]	3.35 (0.00) [0]
974	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A)	3/2020	6/2022 (-) [6/2022]	167.95 (-) [167.95]	1.12 (0.00) [0]
975	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B)	7/2020	8/2022 (-) [8/2022]	177.76 (-) [177.76]	0.64 (0.00) [0]
976	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO	8/2020	4/2022 (-) [4/2022]	268.98 (-) [268.98]	0.00 (0.00) [0]
977	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI	8/2020	4/2022 (-) [4/2022]	228.97 (-) [228.97]	0.00 (0.00) [0]
978	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI	8/2020	4/2022 (-) [4/2022]	379.39 (-) [379.39]	0.00 (0.00) [0]
979	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137	3/2019	7/2022 (-) [7/2022]	471.00 (-) [471.00]	0.00 (0.00) [0]
980	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260.	10/2016	11/2020 (-) [11/2020]	235.31 (-) [235.31]	184.33 (0.00) [0]
981	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	8/2017	10/2018 (-) [10/2021]	517.57 (-) [457.77]	137.04 (-59.80) [36]
	MEGHALAYA				
	Culture Development				
982	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR	4/2014	9/2017 (-) [3/2021]	151.33 (-) [151.33]	148.33 (0.00) [0]
	Health And Family Welfare				
983	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (-) [12/2021]	363.99 (-) [363.99]	239.89 (0.00) [43]
	Human Resource Development				
984	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	9/2013	9/2014 (-) [0/0]	484.32 (-) [626.26]	0.00 (141.94) [0]
	Railways				
985	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [0/0]	906.46 (1,202.33) [4,083.02]	264.33 (3,176.56) [0]
	Road Transport And Highways				
986	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	3/2019	5/2019 (-) [0/0]	306.28 (-) [306.28]	78.34 (0.00) [0]

987	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	12/2015	5/2018 (-) [0/0]	479.20 (-) [479.20]	712.89 (0.00) [0]
988	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	/ (-) [9/2021]	553.51 (-) [553.51]	75.51 (0.00) [-]
	<u>MIZORAM</u>				
	<u>Railways</u>				
989	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (-) [3/2023]	2,393.47 (5,021.45) [5,521.45]	3,954.28 (3,127.98) [108]
	<u>Road Transport And Highways</u>				
990	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (-) [6/2021]	195.04 (-) [377.99]	331.49 (182.95) [128]
991	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	9/2014 (-) [6/2021]	186.96 (-) [322.24]	298.52 (135.28) [81]
992	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (-) [6/2021]	193.69 (-) [327.92]	301.46 (134.23) [128]
993	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54	9/2020	10/2022 (-) [10/2022]	275.02 (-) [275.02]	14.15 (0.00) [0]
994	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I)	3/2020	7/2022 (-) [7/2022]	206.88 (-) [206.88]	9.33 (0.00) [0]
995	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II)	3/2020	7/2022 (-) [7/2022]	216.49 (-) [216.49]	28.93 (0.00) [0]
996	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III)	3/2020	7/2022 (-) [7/2022]	292.24 (-) [292.24]	29.00 (0.00) [0]
997	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV)	3/2020	7/2022 (-) [7/2022]	281.78 (-) [281.78]	38.40 (0.00) [0]
998	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2023]	519.09 (-) [519.09]	56.58 (0.00) [43]
999	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [6/2023]	642.96 (-) [642.96]	82.00 (0.00) [45]
1000	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2023]	473.18 (-) [473.18]	81.00 (0.00) [43]
1001	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [7/2023]	640.07 (-) [640.07]	3.25 (0.00) [46]
1002	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2023]	537.82 (-) [537.82]	100.74 (0.00) [43]
1003	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2024]	404.29 (-) [404.29]	17.77 (0.00) [55]
1004	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2023]	428.11 (-) [428.11]	48.03 (0.00) [48]
1005	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [6/2023]	518.53 (-) [518.53]	108.99 (0.00) [45]
1006	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC	11/2010	3/2011	624.41	890.74

	IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN		(-) [12/2020]	(-) [992.67]	(368.26) [0]
	MULTI STATE				
	Coal				
1007	BINA KAKRI AMALGAMATION OCP 14 MTPA	8/2020	3/2024 (-) [3/2024]	836.42 (-) [836.42]	60.07 (0.00) [0]
1008	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY)	2/2017	3/2021 (-) [9/2023]	328.00 (-) [328.00]	295.83 (0.00) [30]
1009	NILJAI EXPANSION (DEEP) OC (3.5 MTY)	8/2016	3/2022 (-) [3/2022]	319.76 (-) [404.45]	246.02 (84.69) [0]
1010	RECAST PR FOR DHANKASA UG (1.00 MTY)	9/2016	3/2022 (-) [3/2025]	289.29 (-) [289.30]	35.95 (0.01) [36]
	Dpiit				
1011	DELHI MUMBAI INDUSTRIAL CORRIDOR	9/2011	9/2019 (1/2014) [7/2021]	12,579.09 (-) [13,812.30]	8,915.05 (1,233.21) [22]
	Human Resource Development				
1012	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION	8/2018	3/2019 (-) [0/0]	418.00 (-) [418.00]	110.00 (0.00) [0]
1013	STUDY IN INDIA	3/2018	4/2018 (-) [0/0]	150.00 (-) [150.00]	0.00 (0.00) [0]
	Petroleum				
1014	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	1/2015	3/2021 (12/2021) [12/2021]	1,823.00 (3,027.90) [3,027.90]	1,957.55 (1,204.90) [9]
1015	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II	9/2016	12/2019 (-) [8/2021]	571.66 (-) [571.66]	471.81 (0.00) [20]
1016	BARAUNI-GUWAHATI PIPELINE	6/2018	12/2021 (-) [12/2021]	3,308.00 (3,060.00) [3,060.00]	2,272.30 (-248.00) [0]
1017	BARMER PALANPUR PIPELINE	11/2019	11/2022 (-) [11/2022]	776.00 (-) [776.00]	215.96 (0.00) [0]
1018	BOKARO-ANGUL PIPELINE PROJECT	3/2017	12/2020 (12/2021) [12/2021]	3,437.00 (3,048.00) [3,048.00]	1,852.90 (-389.00) [12]
1019	DHAMRA HALDIA PIPELINE PROJECT	3/2020	11/2022 (-) [11/2022]	1,030.65 (-) [1,030.65]	53.10 (0.00) [0]
1020	DOBHI-DURGAPUR PIPELINE PROJECT	3/2017	12/2020 (12/2021) [6/2021]	2,433.00 (-) [2,433.00]	2,110.70 (0.00) [6]
1021	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	9/2017	6/2021 (8/2022) [8/2022]	2,677.00 (-) [3,072.00]	2,239.96 (395.00) [14]
1022	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	6/2009	12/2012 (2/2022) [2/2022]	2,915.00 (5,909.00) [5,909.00]	3,607.20 (2,994.00) [110]
1023	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT	7/2015	12/2020 (-) [9/2021]	2,881.40 (-) [2,000.00]	1,607.70 (-881.40) [9]
1024	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT	6/2020	5/2023 (-) [5/2023]	7,844.25 (-) [7,844.25]	1,079.10 (0.00) [0]

1025	PARADIP HYDERABAD PIPELINE	1/2015	12/2020 (3/2022) [3/2022]	2,321.00 (3,338.00) [3,338.00]	2,923.70 (1,017.00) [15]
1026	PARADIP LPG IMPORT FACILITY	1/2015	7/2018 (5/2021) [5/2021]	690.00 (-) [690.00]	545.44 (0.00) [34]
1027	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I)	5/2016	10/2020 (-) [3/2022]	406.00 (-) [406.00]	225.67 (0.00) [17]
1028	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	7/2011	3/2017 (-) [3/2021]	352.56 (-) [490.24]	455.00 (137.68) [0]
1029	SRIKAKULAM ANGUL PIPELINE PROJECT	9/2019	7/2022 (-) [7/2022]	2,658.34 (-) [2,658.34]	245.50 (0.00) [0]
	Power				
1030	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION)	9/2017	9/2019 (9/2020) [5/2020]	198.49 (-) [198.49]	140.97 (0.00) [0]
1031	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	12/2018 (-) [3/2024]	4,754.42 (9,129.32) [9,129.32]	2,163.30 (4,374.90) [63]
1032	EASTERN REGION STRENGTHENING SCHEME XX	11/2017	5/2020 (5/2021) [5/2021]	358.83 (-) [358.83]	253.49 (0.00) [12]
1033	EASTERN REGION STRENGTHENING SCHEME-V	10/2013	4/2016 (9/2020) [7/2020]	1,364.52 (1,891.41) [1,891.41]	1,326.81 (526.89) [0]
1034	EASTERN REGION STRENGTHENING SCHEME-XII	5/2014	11/2016 (9/2021) [6/2021]	522.29 (546.36) [546.36]	478.29 (24.07) [55]
1035	EASTERN REGION STRENGTHENING SCHEME-XVIII	3/2017	7/2020 (12/2020) [6/2021]	3,500.00 (3,500.00) [3,994.00]	2,917.31 (494.00) [11]
1036	EASTERN REGION STRENGTHENING SCHEME XVII(PART B)	2/2017	6/2019 (8/2021) [6/2021]	235.53 (-) [235.53]	151.12 (0.00) [24]
1037	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/	2/2017	2/2019 (6/2021) [9/2021]	322.30 (-) [322.30]	201.55 (0.00) [31]
1038	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	3/2015	3/2018 (-) [6/2021]	197.40 (-) [197.40]	90.05 (0.00) [39]
1039	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D	5/2016	5/2019 (-) [0/0]	3,519.59 (-) [3,519.59]	2,562.41 (0.00) [0]
1040	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR	2/2017	4/2020 (6/2021) [6/2021]	5,070.13 (-) [5,070.13]	4,101.57 (0.00) [14]
1041	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P	5/2016	11/2019 (4/2021) [6/2021]	14,733.37 (-) [14,733.37]	11,552.37 (0.00) [19]
1042	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN	8/2017	2/2020 (6/2021) [6/2021]	1,931.39 (-) [1,931.39]	1,709.25 (0.00) [16]
1043	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	12/2014	12/2018 (-) [12/2021]	5,111.33 (6,700.00) [6,700.00]	2,767.14 (1,588.67) [36]
1044	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	2/2009	8/2013 (8/2022) [8/2022]	11,130.19 (14,719.10) [14,719.10]	12,894.95 (3,588.91) [108]

1045	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO	3/2017	11/2019 (-) [0/0]	283.72 (-) [283.72]	196.10 (0.00) [0]
1046	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	12/2015	4/2019 (-) [0/0]	3,654.00 (-) [3,654.00]	3,508.04 (0.00) [0]
1047	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	10/2016	4/2019 (-) [0/0]	608.24 (-) [608.24]	425.04 (0.00) [0]
1048	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII	1/2015	7/2017 (-) [0/0]	203.28 (-) [260.03]	200.16 (56.75) [0]
1049	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII	3/2017	12/2019 (6/2021) [9/2021]	379.95 (-) [379.95]	232.02 (0.00) [21]
1050	SYTEM STRENGTHENING XIII OF SR GRID	10/2011	6/2014 (-) [0/0]	487.49 (-) [639.46]	590.30 (151.97) [0]
1051	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	10/2008	10/2012 (11/2020) [3/2021]	4,824.12 (5,071.94) [5,071.94]	4,634.56 (247.82) [0]
1052	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP)	1/2015	10/2017 (5/2021) [1/2021]	871.62 (902.49) [902.49]	648.77 (30.87) [0]
1053	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II)	10/2016	1/2019 (9/2020) [4/2020]	408.46 (516.12) [516.12]	417.12 (107.66) [0]
1054	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH	6/2014	3/2018 (-) [0/0]	5,151.37 (-) [5,151.37]	3,269.93 (0.00) [0]
1055	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	3/2016	1/2018 (4/2021) [5/2021]	808.63 (-) [808.63]	662.19 (0.00) [40]
1056	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	1/2014	4/2016 (12/2017) [6/2021]	374.63 (-) [374.63]	246.80 (0.00) [62]
	<u>Railways</u>				
1057	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT	12/2015	12/2023 (-) [12/2023]	1,08,000.00 (-) [1,08,000.00]	12,039.69 (0.00) [0]
1058	BANDEL-BOINCHI 3RD LINE	4/2011	/ (-) [3/2021]	288.35 (-) [502.48]	432.62 (214.13) [0]
1059	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT	4/2007	/ (-) [3/2025]	450.55 (-) [250.55]	20.11 (-200.00) [-]
1060	BHADRACHALAM ROAD-SATTUPALLI	4/2010	3/2020 (3/2022) [6/2021]	704.31 (-) [927.94]	534.34 (223.63) [15]
1061	BOINCHI-SHAKTIGARH 3RD LINE	4/2011	/ (-) [3/2022]	175.80 (-) [495.10]	288.51 (319.30) [-]
1062	CHANDIGARH-BADDI	4/2007	3/2023 (3/2025) [3/2025]	328.14 (1,540.13) [1,540.13]	242.04 (1,211.99) [24]
1063	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA	4/2003	/ (-) [3/2025]	337.96 (-) [336.96]	70.20 (-1.00) [-]
1064	CHENNAI-CUDDALORE VIA MAMALLAPURAM	4/2008	/ (-) [3/2024]	523.52 (-) [1,205.00]	2.28 (681.48) [-]

1065	CHHAPRA-BALLIA UP	3/2013	1/2019 (-) [2/2022]	295.00 (-) [477.31]	378.98 (182.31) [37]
1066	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP	3/2007	12/2021 (-) [12/2021]	243.78 (-) [895.00]	111.89 (651.22) [0]
1067	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	4/2005	3/2017 (-) [3/2025]	595.51 (-) [769.40]	103.86 (173.89) [96]
1068	CHOTTAUDEPUR-DHAR(NL)	4/2007	3/2022 (3/2023) [3/2023]	1,347.26 (1,347.26) [1,347.26]	907.54 (0.00) [12]
1069	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	4/2007	3/2022 (3/2023) [3/2023]	1,640.04 (1,640.04) [1,640.04]	866.42 (0.00) [12]
1070	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL	4/2010	3/2017 (-) [3/2025]	365.17 (-) [439.30]	411.65 (74.13) [96]
1071	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL	4/2007	/ (-) [3/2023]	336.91 (-) [791.39]	572.99 (454.48) [-]
1072	DEOGHAR - SULTANGANJ (INL), ER	4/2000	2/2013 (-) [3/2024]	607.09 (-) [1,425.44]	638.05 (818.35) [133]
1073	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANPUR AND TANPUR-BANSI PAHARPUR	4/2010	/ (-) [0/0]	2,030.50 (-) [2,030.50]	19.07 (0.00) [0]
1074	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	4/2010	3/2015 (-) [3/2025]	651.00 (-) [1,009.00]	7.96 (358.00) [120]
1075	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	/ (-) [0/0]	11,589.00 (30,357.00) [28,181.00]	0.00 (16,592.00) [0]
1076	GAYA-CHATRA (NL)	4/2008	/ (-) [0/0]	415.67 (-) [549.75]	15.58 (134.08) [0]
1077	GONDIA-JABALPUR(GC),(SECR)	2/1997	4/2020 (-) [4/2021]	511.86 (-) [2,005.25]	1,777.22 (1,493.39) [12]
1078	GOOTY-DHARMAVARAM-BANGLORE	4/2015	/ (-) [0/0]	636.38 (-) [636.38]	0.00 (0.00) [0]
1079	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	4/2011	3/2022 (-) [12/2024]	2,912.96 (-) [3,845.60]	148.26 (932.64) [33]
1080	HAJIPUR - BACHAWARA	5/2015	3/2019 (-) [5/2021]	678.54 (678.54) [929.86]	848.39 (251.32) [26]
1081	HANSDIHA-GODDA NL	4/2011	3/2020 (-) [3/2021]	542.18 (-) [663.13]	534.85 (120.95) [0]
1082	HANSNABAD-HINGALGANJ NEW BG LINE	4/2010	/ (-) [3/2025]	172.03 (-) [260.10]	11.74 (88.07) [-]
1083	HATHUA-BHATNI (N L) (NER)	4/2005	12/2022 (-) [12/2022]	230.03 (-) [230.03]	277.14 (0.00) [0]
1084	HOTGI-KUDGI-GADAG	3/2015	3/2019 (3/2024) [3/2024]	1,614.59 (-) [1,870.41]	1,341.15 (255.82) [60]
1085	HOWRAH DIVISION- PLATFORM SHELTER (40 C	4/2010	11/2018	157.94	51.74

	CATEGORY STATIONS)		(-) [3/2021]	(-) [157.94]	(0.00) [0]
1086	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES	4/2011	/	166.89	0.02
			(-) [3/2025]	(-) [166.89]	(0.00) [-]
1087	JALANDHAR-PATHANKOT-JAMMU TAWI	3/2002	3/2016	625.00	852.73
			(-) [6/2021]	(-) [859.00]	(234.00) [63]
1088	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	4/2008	3/2014	2,132.77	350.54
			(-) [3/2027]	(-) [3,037.95]	(905.18) [156]
1089	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3	4/2001	3/2016	923.52	645.97
			(-) [3/2025]	(-) [995.10]	(71.58) [108]
1090	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE	4/2010	/	174.56	71.43
			(-) [3/2025]	(-) [174.56]	(0.00) [-]
1091	KAZIPET-BALHRSHA	4/2015	3/2021	2,063.03	1,416.78
			(-) [3/2024]	(-) [2,063.03]	(0.00) [36]
1092	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	4/2012	3/2023	1,856.95	567.51
			(-) [3/2024]	(-) [1,952.68]	(95.73) [12]
1093	KURUPPANTHARA-CHINGAVANAM	4/2007	/	270.14	439.49
			(-) [12/2021]	(-) [457.08]	(186.94) [-]
1094	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	4/1987	3/2006	406.99	149.31
			(-) [3/2025]	(-) [545.70]	(138.71) [228]
1095	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	9/1998	5/2008	247.66	2,131.17
			(-) [3/2025]	(-) [8,248.50]	(8,000.84) [202]
1096	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL	4/2009	3/2014	257.42	107.35
			(-) [3/2025]	(-) [257.42]	(0.00) [132]
1097	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI	4/2011	3/2019	120.70	262.36
			(-) [12/2027]	(-) [2,172.16]	(2,051.46) [105]
1098	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	4/2009	2/2012	499.96	164.09
			(-) [3/2025]	(-) [680.68]	(180.72) [157]
1099	MONIGRAM- NIMTITA	4/2012	/	250.93	293.10
			(-) [3/2024]	(-) [310.70]	(59.77) [-]
1100	MUNEERABAD-MAHABOBNAGAR(NL),SCR	4/1997	3/2000	1,723.00	1,895.77
			(-) [3/2023]	(1.00) [3,421.35]	(1,698.35) [276]
1101	MURKONGSELEK-PASIGHAT NL	4/2011	3/2020	414.84	156.54
			(-) [0/0]	(-) [1,040.00]	(625.16) [0]
1102	NANGALDAM-TALWARA(NL),NR	3/1981	7/2012	450.00	714.78
			(-) [3/2024]	(-) [2,200.00]	(1,750.00) [140]
1103	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL	4/2010	3/2005	494.54	32.00
			(-) [3/2025]	(-) [494.59]	(0.05) [240]
1104	NEW BG LINE FROM BALURGHAT TO HILLY NFR	4/2010	3/2020	242.22	76.56
			(-) [0/0]	(-) [471.00]	(228.78) [0]
1105	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	4/2010	/	241.52	287.09
			(-)	(-)	(132.35)

			[12/2021]	[373.87]	[-]
1106	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	4/2013	3/2019 (-) [3/2024]	1,798.00 (2,042.51) [2,042.51]	136.41 (244.51) [60]
1107	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	4/1999	/ (-) [0/0]	819.23 (-) [1,871.00]	1,082.01 (1,051.77) [0]
1108	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	4/2000	12/2008 (-) [5/2021]	1,180.19 (2,531.34) [4,541.38]	3,804.55 (3,361.19) [149]
1109	PHULERA - DIGANA DOUBLING	5/2015	3/2020 (-) [10/2022]	600.00 (-) [701.81]	236.13 (101.81) [31]
1110	PIRPAINTI-BHAGALPUR	4/2011	/ (-) [5/2019]	261.38 (-) [565.00]	547.01 (303.62) [0]
1111	PIRPAINTI-JASIDIH	4/2013	3/2022 (-) [3/2025]	915.98 (-) [2,137.81]	388.53 (1,221.83) [36]
1112	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY	4/2011	3/2017 (-) [3/2026]	299.60 (-) [335.62]	1.12 (36.02) [108]
1113	RATLAM-DUNGARPUR VIA BANSWARA (NL)	4/2011	/ (-) [0/0]	2,082.75 (-) [4,262.36]	186.12 (2,179.61) [0]
1114	RAYADURGA-TUMKUR NL	4/2007	/ (-) [3/2025]	2,062.30 (-) [2,432.50]	1,127.71 (370.20) [-]
1115	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL	4/2000	/ (-) [3/2025]	297.47 (-) [298.22]	52.09 (0.75) [-]
1116	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	4/2010	3/2016 (-) [3/2025]	277.28 (-) [266.32]	191.22 (-10.96) [108]
1117	SRINIVASA-PURA-MADANAPALLI NL	4/2013	/ (-) [12/2023]	296.00 (-) [296.10]	0.01 (0.10) [-]
1118	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR	4/2007	/ (-) [3/2025]	450.00 (-) [1,261.34]	0.00 (811.34) [-]
1119	TARAKESHWAR-MAGRA NEW BG LINE	4/2010	/ (-) [3/2025]	365.17 (-) [527.54]	1.76 (162.37) [-]
1120	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	3/2020 (-) [0/0]	16,592.00 (51,101.00) [51,101.00]	22,485.00 (34,509.00) [0]
1121	YELAHANKA-PENUKONDA	5/2015	3/2020 (-) [6/2021]	860.43 (-) [1,147.00]	911.86 (286.57) [15]
	<u>Road Transport And Highways</u>				
1122	4 LANING OF NAGPUR-BETUL	2/2011	8/2014 (-) [0/0]	2,498.76 (-) [2,498.76]	2,531.46 (0.00) [0]
1123	DELHI AGRA APPROVED LENGTH 180.0 KM	10/2012	4/2015 (1/2021) [6/2021]	1,928.22 (-) [3,182.34]	3,087.00 (1,254.12) [74]
1124	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67.	3/2018	/ (-) [0/0]	1,294.47 (-) [1,296.00]	0.00 (1.53) [0]
1125	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM	3/2018	/ (-)	998.70 (-)	0.00 (-36.70)

	29.000 (DE		[0/0]	[962.00]	[0]
1126	GWALIOR-JHANSI, NH-75	12/2003	12/2009 (-) [0/0]	604.00 (-) [364.59]	334.71 (-239.41) [0]
1127	MUZAFFARNAGAR-HARIDWAR	9/2011	3/2013 (-) [0/0]	754.00 (-) [754.00]	1,364.18 (0.00) [0]
1128	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP	9/2016	/ (-) [5/2021]	1,244.10 (-) [1,244.10]	1,590.00 (0.00) [-]
1129	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	2/2009	8/2011 (-) [0/0]	1,693.75 (-) [1,693.75]	2,848.49 (0.00) [0]
1130	VARANASI-AURANGABAD KM.786 TO KM.978.40	9/2011	3/2014 (-) [12/2022]	2,848.00 (-) [3,379.45]	2,901.20 (531.45) [105]
	<u>Shipping And Ports</u>				
1131	JAL MARG VIKAS PROJECT	1/2018	3/2023 (-) [3/2023]	5,369.18 (-) [4,633.81]	1,871.35 (-735.37) [0]
	<u>Telecommunications</u>				
1132	NETWORK FOR SPECTRUM	3/2012	7/2015 (-) [7/2021]	13,334.00 (-) [24,664.00]	17,845.00 (11,330.00) [72]
1133	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART	3/2020	6/2021 (-) [11/2021]	431.16 (431.00) [431.16]	0.00 (0.00) [5]
	<u>Urban Development</u>				
1134	DELHI GHAZIABAD MEERUT RRTS CORRIDOR	3/2019	6/2025 (-) [6/2025]	30,274.00 (-) [30,274.00]	3,416.31 (0.00) [0]
	<u>NAGALAND</u>				
	<u>Railways</u>				
1135	DIMAPUR-TIZIT NL	4/2013	3/2020 (-) [0/0]	4,274.00 (-) [4,274.00]	0.00 (0.00) [0]
1136	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015 (-) [12/2024]	2,326.52 (-) [6,911.00]	1,204.64 (4,584.48) [117]
	<u>Road Transport And Highways</u>				
1137	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018 (-) [5/2022]	239.30 (-) [239.30]	102.01 (0.00) [44]
1138	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	3/2018	9/2018 (-) [9/2022]	285.68 (-) [285.68]	77.91 (0.00) [48]
1139	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	3/2018	9/2018 (-) [0/0]	282.98 (-) [192.60]	127.31 (-90.38) [0]
1140	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018 (-) [9/2020]	387.00 (-) [387.00]	283.11 (0.00) [0]
1141	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	9/2018 (-) [11/2022]	500.09 (336.49) [336.49]	79.51 (-163.60) [50]
1142	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I)	3/2020	6/2022 (-) [6/2022]	320.97 (-) [320.97]	18.73 (0.00) [0]
1143	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II)	3/2020	6/2022 (-) [6/2022]	355.79 (-) [355.79]	31.76 (0.00) [0]

1144	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III)	3/2020	6/2022 (-) [6/2022]	361.53 (-) [361.53]	13.17 (0.00) [0]
1145	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV)	3/2020	12/2021 (-) [12/2021]	330.78 (-) [330.78]	23.74 (0.00) [0]
1146	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V)	4/2020	12/2021 (-) [12/2021]	330.80 (-) [330.80]	11.57 (0.00) [0]
1147	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I)	3/2020	6/2022 (-) [6/2022]	278.95 (-) [278.95]	56.76 (0.00) [0]
1148	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN	3/2017	11/2020 (5/2021) [11/2020]	217.35 (-) [217.35]	97.62 (0.00) [0]
1149	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T	9/2020	4/2022 (-) [4/2022]	257.15 (-) [257.15]	17.77 (0.00) [0]
1150	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES	8/2020	4/2022 (-) [4/2022]	202.36 (-) [202.36]	0.00 (0.00) [0]
1151	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D	8/2020	4/2022 (-) [4/2022]	232.29 (-) [232.29]	0.00 (0.00) [0]
1152	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D	9/2020	10/2022 (-) [10/2022]	277.44 (-) [277.44]	0.00 (0.00) [0]
1153	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG	8/2020	10/2022 (-) [10/2022]	159.85 (-) [159.85]	0.00 (0.00) [0]
1154	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683	2/2017	4/2017 (-) [0/0]	507.68 (-) [507.68]	129.13 (0.00) [0]
1155	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [7/2022]	339.57 (-) [339.57]	141.46 (0.00) [46]
1156	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	3/2018	9/2018 (-) [12/2021]	315.03 (-) [315.03]	88.52 (0.00) [39]
1157	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	9/2018 (-) [12/2021]	240.64 (-) [240.64]	102.51 (0.00) [39]
1158	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [11/2021]	215.12 (-) [215.12]	100.90 (0.00) [38]
1159	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	9/2018 (-) [12/2021]	215.79 (-) [215.79]	67.30 (0.00) [39]
1160	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [10/2022]	272.89 (-) [272.89]	51.17 (0.00) [49]
1161	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	3/2018	9/2018 (-) [11/2022]	323.98 (-) [323.98]	42.54 (0.00) [50]
1162	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0	3/2018	9/2018 (-) [0/0]	251.97 (-) [251.97]	138.60 (0.00) [0]
1163	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (-) [0/0]	237.72 (-) [237.72]	109.96 (0.00) [0]
1164	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM	3/2016	8/2016	373.07	245.80

	DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1		(-) [5/2021]	(-) [387.00]	(13.93) [57]
1165	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2016 (-) [5/2021]	396.52 (-) [339.55]	252.49 (-56.97) [57]
1166	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	3/2016	8/2016 (-) [5/2021]	429.52 (-) [340.00]	193.99 (-89.52) [57]
1167	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M	11/2016	9/2019 (11/2020) [0/0]	336.25 (369.96) [336.25]	322.13 (0.00) [0]
1168	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (9/2021) [12/2020]	167.62 (-) [167.62]	104.39 (0.00) [0]
1169	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (9/2021) [12/2020]	172.63 (-) [172.63]	129.65 (0.00) [0]
1170	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM	9/2020	4/2022 (-) [4/2022]	315.63 (-) [315.63]	0.00 (0.00) [0]
1171	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA	12/2010	2/2011 (-) [0/0]	1,296.00 (-) [1,296.00]	0.00 (0.00) [0]
1172	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH-	3/2019	12/2022 (-) [12/2022]	237.51 (-) [237.51]	60.04 (0.00) [0]
	<u>ODISHA</u>				
	<u>Coal</u>				
1173	ANANTA OC EXPANSION PH-III (15.0 MTY)	8/2008	3/2012 (-) [3/2021]	207.28 (-) [207.28]	168.13 (0.00) [0]
1174	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	5/2014	3/2019 (-) [3/2024]	479.15 (-) [479.15]	278.53 (0.00) [60]
1175	BHUBANESWARI EXPENSION OCP(40.0 MTY)	12/2007	3/2017 (-) [3/2031]	3,145.45 (-) [3,145.45]	612.55 (0.00) [168]
1176	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY)	12/2007	3/2010 (3/2029) [3/2029]	3,504.21 (3,504.21) [3,504.21]	607.83 (0.00) [228]
1177	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY)	12/2007	3/2013 (3/2028) [3/2028]	8,416.19 (8,416.19) [8,416.19]	890.78 (0.00) [180]
1178	GARJANBAHAL OCP	11/2014	3/2021 (-) [3/2024]	1,375.38 (-) [1,375.38]	504.36 (0.00) [36]
1179	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	3/2013 (-) [3/2022]	479.53 (-) [479.53]	475.14 (0.00) [108]
1180	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP	5/2018	3/2027 (-) [3/2027]	2,434.75 (-) [2,434.75]	181.04 (0.00) [0]
1181	REORGANISATION OF BHARATPUR OCP EXPANSION	11/2018	3/2029 (-) [3/2029]	2,838.87 (-) [2,838.87]	1,236.90 (0.00) [0]
1182	SIARMAL OCP (40.00MTY)	5/2014	3/2026 (-) [3/2026]	3,756.36 (-) [3,756.36]	1,986.09 (0.00) [0]
1183	TALABIRA II AND III OCP	7/2017	7/2020 (-) [4/2020]	2,401.07 (-) [2,401.07]	861.37 (0.00) [0]

	<u>Human Resource Development</u>				
1184	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR	1/2019	3/2022 (-) [6/2022]	790.79 (-) [790.79]	173.98 (0.00) [3]
	<u>Mines</u>				
1185	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/2014	4/2021 (12/2022) [12/2022]	5,540.00 (6,435.90) [5,540.00]	731.55 (0.00) [20]
1186	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	12/2015	11/2020 (-) [2/2021]	355.00 (-) [355.00]	94.80 (0.00) [0]
1187	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN	11/2017	4/2021 (3/2023) [3/2023]	483.00 (483.00) [483.00]	0.92 (0.00) [23]
1188	UTKAL D AND E COAL BLOCK	5/2016	1/2020 (-) [0/0]	534.00 (-) [534.00]	338.79 (0.00) [0]
	<u>Petroleum</u>				
1189	2ND GENERATION LIGNOCELLULOSIC BIOMASS ETHANOL BIOFUEL REFINERY AT BARGARH (ODISHA)	8/2019	8/2022 (-) [8/2022]	1,607.00 (-) [1,607.00]	255.22 (0.00) [0]
1190	ADDITIONAL STORAGE TANKS AT PARADIP	11/2018	9/2021 (6/2022) [6/2022]	462.30 (-) [462.30]	23.19 (0.00) [9]
1191	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY	8/2017	12/2021 (-) [8/2021]	315.00 (-) [315.00]	208.09 (0.00) [-4]
1192	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR	7/2017	7/2022 (-) [7/2022]	243.53 (-) [243.53]	115.28 (0.00) [0]
1193	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK	7/2017	7/2022 (-) [7/2022]	182.20 (-) [182.20]	78.03 (0.00) [0]
1194	DHAMRA-ANGUL PIPELINE PROJECT	3/2017	12/2020 (12/2021) [12/2021]	1,933.00 (-) [1,933.00]	1,268.75 (0.00) [12]
1195	ETHYLENE GLYCOL PROJECT AT PARADIP	4/2018	10/2021 (-) [10/2021]	5,654.00 (-) [5,654.00]	2,826.29 (0.00) [0]
1196	Fuel Quality Upgradation Project at Paradip Refinery	5/2019	8/2021 (9/2022) [9/2022]	3,361.00 (-) [3,361.00]	1,665.03 (0.00) [13]
1197	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY	1/2020	7/2022 (-) [7/2022]	202.16 (-) [202.16]	18.34 (0.00) [0]
1198	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY	6/2019	9/2022 (3/2023) [3/2023]	371.00 (-) [371.00]	4.44 (0.00) [6]
1199	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY	7/2020	1/2024 (-) [1/2024]	13,805.00 (-) [13,805.00]	92.75 (0.00) [0]
1200	LPG BP PROJECT KHORDHA	12/2016	12/2019 (3/2022) [3/2022]	161.59 (-) [161.59]	49.59 (0.00) [27]
1201	PARADIP SOMNATHPUR HALDIA PIPELINE	10/2018	10/2021 (-) [3/2022]	1,297.50 (-) [1,297.50]	722.93 (0.00) [5]
	<u>Power</u>				
1202	DARLIPALLI STPP STAGE-I (2X800 MW)	2/2014	12/2018 (5/2021) [5/2021]	12,532.44 (13,140.91) [13,140.91]	11,730.23 (608.47) [29]

1203	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL	5/2016	12/2018 (-) [7/2021]	1,885.13 (-) [1,885.13]	1,763.69 (0.00) [31]
	<u>Railways</u>				
1204	BANASPANI- JAKHPURA - DOUBLING	3/2009	3/2019 (-) [6/2022]	942.95 (-) [1,536.00]	1,089.84 (593.05) [39]
1205	BHADRAK - NERGUNDI 3RD LINE	3/2013	10/2020 (3/2024) [3/2024]	843.04 (843.04) [843.04]	227.52 (0.00) [41]
1206	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	4/2015	12/2018 (3/2024) [3/2024]	1,172.92 (1,172.92) [1,172.92]	613.52 (0.00) [63]
1207	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION	4/2010	3/2015 (-) [0/0]	149.90 (-) [230.00]	54.46 (80.10) [0]
1208	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL	4/2016	3/2020 (-) [3/2024]	5,200.00 (-) [962.00]	54.75 (-4,238.00) [48]
1209	HARIDASPUR-PARADEEP(NL)	4/1996	12/2017 (-) [0/0]	1,185.64 (-) [1,844.47]	1,883.44 (658.83) [0]
1210	JAGADALPUR-KORAPUT DOUBLING	4/2015	3/2022 (3/2023) [3/2023]	1,547.38 (1,547.38) [1,547.38]	612.77 (0.00) [12]
1211	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	4/2015	11/2018 (-) [3/2024]	701.61 (-) [810.02]	171.45 (108.41) [64]
1212	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	4/2000	3/2009 (3/2009) [0/0]	133.41 (207.00) [396.00]	388.21 (262.59) [0]
1213	KHURDA ROAD-BOLANGIR(NL)ECOR	4/1994	3/2009 (3/2026) [3/2026]	2,923.13 (3,791.66) [3,791.66]	1,506.95 (868.53) [204]
1214	KORAPUT - SINGAPUR ROAD DOUBLING	4/2015	3/2022 (3/2026) [3/2026]	2,361.74 (2,361.74) [2,361.74]	432.17 (0.00) [48]
1215	ROURKELA JHARSUGUDA THIRD LINE 101 KM	11/2015	3/2020 (3/2020) [12/2021]	969.83 (1,312.96) [1,312.96]	940.00 (343.13) [21]
1216	SAMBALPUR - ANGUL RLY. ELECTRIFICATION	3/2012	3/2020 (3/2021) [3/2022]	155.81 (238.03) [238.03]	221.48 (82.22) [24]
1217	SAMBALPUR - TITLAGARH - DOUBLING	3/2006	3/2020 (-) [12/2021]	948.04 (-) [2,009.00]	1,875.48 (1,060.96) [21]
1218	SAMBALPUR-TALCHER DOUBLING	3/2011	2/2019 (-) [12/2021]	1,111.99 (-) [1,539.28]	1,109.06 (427.29) [34]
1219	SUKINDA ROAD - ANGUL (NL)(ECOR)	4/1998	2/2015 (-) [6/2022]	1,202.70 (-) [2,440.53]	1,337.54 (1,237.83) [88]
1220	TALCHER-BIMALAGARH(NL)(ECOR)	4/2005	6/2021 (3/2025) [3/2025]	810.78 (1,928.07) [1,928.07]	873.81 (1,117.29) [45]
1221	VIZIANAGARAM -SAMABALPUR 3RD LINE	1/1991	12/2024 (-) [12/2026]	2,335.67 (-) [3,327.72]	1,317.36 (992.05) [24]
	<u>Road Transport And Highways</u>				
1222	4 LANING OF BAHARAGORA - SINGHARA	7/2015	/	1,282.94	468.69
			(-)	(-)	(0.00)

			[3/2021]	[1,282.94]	[0]
1223	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S	9/2016	8/2019 (-) [3/2021]	2,510.04 (-) [2,510.04]	555.68 (0.00) [0]
1224	FOUR LANING WITH PS TALEBANI -SMBALPUR	12/2015	/ (-) [3/2022]	752.28 (-) [752.28]	213.52 (0.00) [-]
1225	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION	2/2016	/ (-) [1/2021]	1,069.65 (-) [1,069.65]	611.71 (0.00) [0]
1226	PANIKHOLI-RIMOLI	3/2012	9/2014 (-) [0/0]	1,410.00 (-) [1,410.00]	1,935.14 (0.00) [0]
1227	REHABILITAITON AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4	10/2016	/ (-) [6/2021]	1,008.96 (-) [1,008.96]	930.39 (0.00) [-]
1228	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS	1/2018	/ (-) [8/2021]	564.66 (-) [564.66]	240.00 (0.00) [-]
1229	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	7/2017	7/2017 (-) [6/2021]	476.56 (-) [476.56]	52.19 (0.00) [47]
1230	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (	1/2018	/ (-) [0/0]	633.68 (-) [633.68]	63.98 (0.00) [0]
1231	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25	1/2018	/ (-) [3/2022]	953.09 (-) [953.09]	332.04 (0.00) [-]
1232	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2	1/2018	/ (-) [6/2021]	668.86 (-) [668.86]	276.59 (0.00) [-]
1233	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG	1/2018	/ (-) [8/2021]	614.48 (-) [614.48]	217.40 (0.00) [-]
1234	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH	7/2014	1/2017 (-) [0/0]	342.05 (-) [342.05]	258.91 (0.00) [0]
1235	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (	1/2018	/ (-) [6/2021]	503.88 (-) [503.88]	25.40 (0.00) [-]
1236	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	3/2017	3/2020 (-) [6/2021]	1,288.07 (-) [1,420.00]	842.24 (131.93) [15]
1237	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO	12/2017	/ (-) [6/2021]	686.65 (-) [686.65]	227.63 (0.00) [-]
1238	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON	1/2018	/ (-) [6/2021]	686.65 (-) [686.65]	261.74 (0.00) [-]
1239	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA	12/2017	/ (-) [6/2021]	417.51 (-) [417.51]	127.61 (0.00) [-]
1240	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN	7/2014	1/2017 (-) [0/0]	342.05 (342.00) [342.00]	258.91 (-0.05) [0]
1241	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141	1/2018	/ (-) [6/2021]	999.00 (-) [999.00]	102.70 (0.00) [-]
1242	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR	8/2013	6/2016 (-) [0/0]	171.96 (172.00) [172.00]	88.30 (0.04) [0]

1243	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB	1/1991	10/2017 (-) [0/0]	218.63 (-) [218.63]	29.27 (0.00) [0]
1244	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK	1/1991	5/2018 (-) [0/0]	229.41 (-) [229.41]	6.65 (0.00) [0]
1245	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK	1/2018	/ (-) [6/2021]	1,522.00 (-) [1,522.00]	304.40 (0.00) [-]
1246	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	12/2011	6/2014 (-) [3/2021]	1,047.00 (-) [1,047.00]	1,874.43 (0.00) [0]
1247	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000)	3/2018	/ (-) [4/2021]	806.11 (-) [806.11]	189.70 (0.00) [-]
1248	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO	3/2014	5/2016 (-) [0/0]	191.50 (192.00) [192.00]	136.19 (0.50) [0]
1249	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM	2/2015	10/2017 (-) [0/0]	239.91 (240.00) [160.00]	147.25 (-79.91) [0]
1250	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY W	1/2015	4/2018 (-) [0/0]	326.63 (327.00) [326.63]	249.26 (0.00) [0]
1251	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG	6/2016	6/2018 (-) [0/0]	157.30 (157.00) [157.30]	97.29 (0.00) [0]
1252	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA	12/2011	11/2017 (-) [0/0]	159.39 (-) [159.39]	210.29 (0.00) [0]
1253	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA	12/2011	8/2015 (-) [0/0]	191.08 (-) [191.08]	99.98 (0.00) [0]
1254	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA.	8/2016	2/2017 (-) [0/0]	287.70 (-) [287.70]	153.90 (0.00) [0]
1255	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA	3/2018	8/2018 (-) [0/0]	214.23 (-) [214.23]	23.44 (0.00) [0]
1256	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26.	3/2016	12/2016 (-) [0/0]	165.06 (-) [165.06]	92.59 (0.00) [0]
1257	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA	12/2016	8/2018 (-) [0/0]	223.50 (-) [223.50]	44.52 (0.00) [0]
1258	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA	3/2018	8/2018 (-) [0/0]	199.16 (-) [199.16]	25.63 (0.00) [0]
1259	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA	9/2016	2/2017 (-) [0/0]	295.67 (-) [295.67]	127.75 (0.00) [0]
1260	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA	12/2016	4/2018 (-) [0/0]	206.88 (-) [206.88]	41.69 (0.00) [0]
	<u>Steel</u>				
1261	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY	11/2020	5/2023 (-) [5/2023]	377.18 (-) [377.18]	32.76 (0.00) [0]
	<u>PONDICHERRY</u>				
	<u>Health And Family Welfare</u>				
1262	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES	3/2018	9/2020	195.00	16.41

	HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT		(-) [4/2022]	(-) [195.00]	(0.00) [19]
	<u>PUNJAB</u>				
	<u>Fertilisers</u>				
1263	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA	1/2018	11/2019 (5/2021) [4/2021]	218.83 (-) [218.83]	191.30 (0.00) [17]
1264	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL	1/2018	11/2019 (5/2021) [4/2021]	239.81 (-) [239.81]	199.11 (0.00) [17]
	<u>Health And Family Welfare</u>				
1265	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	7/2016	6/2020 (-) [7/2021]	703.00 (-) [557.48]	469.13 (-145.52) [13]
1266	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	7/2016	2/2018 (-) [3/2021]	152.95 (-) [177.92]	164.17 (24.97) [0]
	<u>Human Resource Development</u>				
1267	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB.	10/2019	5/2022 (-) [8/2022]	348.24 (-) [348.24]	18.71 (0.00) [3]
1268	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	1/2018	5/2020 (-) [2/2022]	430.00 (-) [387.83]	199.99 (-42.17) [21]
1269	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	8/2016	4/2019 (-) [5/2021]	294.00 (-) [350.69]	276.69 (56.69) [25]
	<u>Petroleum</u>				
1270	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB	5/2020	2/2023 (-) [2/2023]	1,421.46 (-) [1,244.50]	76.19 (-176.96) [0]
	<u>Railways</u>				
1271	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI	6/2009	8/2016 (-) [8/2025]	404.00 (-) [404.00]	226.25 (0.00) [108]
1272	QADIAN-BEAS	4/2011	/ (-) [3/2024]	205.22 (-) [841.90]	1.73 (636.68) [-]
	<u>Road Transport And Highways</u>				
1273	4 LANING FROM PHAGWARA TO RUPNAGAR	8/2016	/ (-) [0/0]	1,169.61 (-) [2,280.00]	1,282.04 (1,110.39) [0]
1274	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600	11/2015	/ (-) [0/0]	847.02 (-) [847.02]	795.30 (0.00) [0]
1275	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00	11/2015	/ (-) [12/2020]	889.24 (-) [904.82]	754.06 (15.58) [0]
1276	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	8/2016	9/2019 (-) [0/0]	1,388.34 (-) [2,587.50]	1,569.38 (1,199.16) [0]
1277	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN	3/2017	3/2020 (-) [12/2021]	754.54 (-) [756.27]	379.05 (1.73) [21]
1278	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS	12/2015	/ (-) [0/0]	766.36 (-) [766.36]	685.36 (0.00) [0]
1279	FOUR LANING OF CHANDIGARH - KHARAR	10/2015	12/2017 (-) [0/0]	447.29 (-) [746.43]	676.33 (299.14) [0]
1280	FOUR LANING OF EXISTING TWO LANE WITH PS FROM	2/2018	/	261.76	200.74

	TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB		(-) [7/2021]	(-) [207.00]	(-54.76) [-]
1281	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION	9/2014	/	479.00	456.80
			(-) [7/2021]	(-) [479.00]	(0.00) [-]
1282	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200	10/2017	10/2019	1,069.59	692.14
			(-) [8/2021]	(-) [1,069.59]	(0.00) [22]
1283	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI	3/2018	/	196.05	143.03
			(-) [0/0]	(-) [196.05]	(0.00) [0]
1284	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN	3/2018	/	199.90	124.52
			(-) [0/0]	(-) [199.90]	(0.00) [0]
1285	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000	3/2018	11/2020	170.57	54.53
			(-) [5/2021]	(-) [170.57]	(0.00) [6]
1286	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF	3/2018	6/2020	173.24	114.55
			(-) [0/0]	(-) [173.24]	(0.00) [0]
1287	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH	3/2018	7/2020	322.48	271.72
			(-) [8/2021]	(-) [322.48]	(0.00) [13]
1288	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES	3/2018	8/2020	293.64	28.24
			(-) [0/0]	(-) [293.64]	(0.00) [0]
1289	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES	3/2018	8/2020	293.64	246.29
			(-) [0/0]	(-) [293.64]	(0.00) [0]
1290	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA	3/2018	8/2020	293.10	156.80
			(-) [0/0]	(-) [293.10]	(0.00) [0]
1291	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA	6/2015	/	892.17	648.44
			(-) [0/0]	(-) [892.17]	(0.00) [0]
	RAJASTHAN				
	Atomic Energy				
1292	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016	12,320.00	13,206.00
			(-) [3/2023]	(-) [17,079.00]	(4,759.00) [75]
	Coal				
1293	BARSINGSAR THERMAL POWER STATION EXTENSION	3/2015	9/2020	2,112.60	140.80
			(-) [0/0]	(-) [2,112.60]	(0.00) [0]
1294	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	3/2015	12/2019	513.63	175.30
			(-) [0/0]	(-) [513.63]	(0.00) [0]
1295	BITHNOK LIGNITE THERMAL POWER STATION	3/2015	9/2020	2,196.30	140.80
			(-) [0/0]	(-) [2,196.30]	(0.00) [0]
1296	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	3/2015	9/2019	522.45	9.88
			(-) [0/0]	(-) [522.45]	(0.00) [0]
	Human Resource Development				
1297	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	12/2016	7/2019	549.31	458.38
			(-) [0/0]	(-) [559.47]	(10.16) [0]
	Petroleum				
1298	LPG BP PROJECT JODHPUR	3/2018	/	229.80	81.48
			(5/2022) [5/2022]	(-) [229.80]	(0.00) [-]

	Power				
1299	FATEHGARH SOLAR 296MW	3/2020	9/2021 (-) [9/2021]	1,749.31 (-) [1,749.31]	0.00 (0.00) [0]
1300	JETSAR SOLAR 160 MW	12/2019	3/2021 (-) [0/0]	702.28 (-) [702.28]	0.00 (0.00) [0]
1301	SAMBHU KI BHURJ SOLAR 250 MW	1/2020	9/2021 (1/2022) [1/2022]	1,522.71 (-) [1,522.71]	437.60 (0.00) [4]
1302	SAMBHU KI BHURJ-II SOLAR 300MW	3/2020	9/2021 (1/2022) [1/2022]	1,782.00 (-) [1,782.00]	200.75 (0.00) [4]
	Railways				
1303	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	5/2015	/ (-) [0/0]	873.71 (-) [1,980.21]	4.60 (1,106.50) [0]
1304	AJMER-BANGURGRAM	4/2011	11/2019 (-) [3/2021]	213.39 (-) [375.00]	348.55 (161.61) [0]
1305	AJMER-KOTA (NASIRABAD-JAUNDRI)	4/2013	/ (-) [0/0]	822.00 (-) [1,099.00]	0.00 (277.00) [0]
1306	ALWAR-BANDIKUI DOUBLING	4/2013	2/2019 (-) [2/2020]	242.09 (-) [525.00]	460.83 (282.91) [0]
1307	BANGURGRAM-GURIYA PATCH DOUBLING	4/2012	12/2019 (-) [2/2021]	246.08 (-) [395.00]	348.47 (148.92) [0]
1308	DAUSA-GANGAPUR CITY(NL),NWR	2/1997	2/2019 (-) [6/2022]	410.08 (-) [860.41]	709.62 (450.33) [40]
1309	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM)	8/2018	8/2022 (-) [11/2022]	808.85 (-) [808.85]	232.42 (0.00) [3]
1310	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR	4/2013	3/2020 (-) [6/2021]	420.18 (-) [480.00]	357.41 (59.82) [15]
1311	MULTI MODAL LOGISTICS PARK AT KATHUWAS	1/2011	3/2018 (-) [0/0]	493.17 (-) [493.17]	464.53 (0.00) [0]
1312	PUSHKAR-MERTA	4/2013	/ (-) [0/0]	323.00 (-) [432.22]	0.00 (109.22) [0]
1313	THIYAT HAMIRA-SANU	4/2013	10/2018 (-) [1/2020]	236.93 (-) [350.45]	273.79 (113.52) [0]
	Road Transport And Highways				
1314	NAGAU-BIKANER SECTION FROM KM 177.00 TO KM 267.325 ON NH-89	3/2020	8/2022 (-) [8/2022]	370.36 (-) [370.36]	90.45 (0.00) [0]
1315	2 LANING WITH PS OF GULABPURA - UNIARA	10/2015	10/2017 (-) [0/0]	597.00 (-) [597.00]	587.64 (0.00) [0]
1316	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA	11/2012	8/2016 (-) [6/2020]	530.07 (-) [530.07]	556.02 (0.00) [0]
1317	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A	7/2016	/ (-) [0/0]	688.70 (-) [688.70]	870.48 (0.00) [0]
1318	6-LANNING OF KISHANGARH TO GULABPURA SECTION	12/2016	/	1,031.95	374.05

	OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE-		(-) [9/2021]	(-) [1,031.95]	(0.00) [-]
1319	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN.	3/2019	/	178.13	139.26
			(-) [3/2021]	(-) [178.13]	(0.00) [0]
1320	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM	8/2014	4/2018	822.90	1,688.16
			(-) [0/0]	(-) [822.90]	(0.00) [0]
1321	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM	3/2018	/	1,158.35	611.28
			(-) [0/0]	(-) [1,158.35]	(0.00) [0]
1322	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709	11/2017	4/2018	163.95	116.47
			(-) [3/2021]	(-) [163.95]	(0.00) [0]
1323	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH.	2/2018	/	716.76	610.56
			(-) [0/0]	(-) [716.76]	(0.00) [0]
1324	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA	2/2018	/	741.86	168.78
			(-) [0/0]	(-) [741.86]	(0.00) [0]
1325	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO	12/2017	/	1,308.73	330.46
			(-) [0/0]	(-) [1,308.73]	(0.00) [0]
1326	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM	6/2016	6/2019	763.23	191.80
			(-) [0/0]	(-) [763.23]	(0.00) [0]
1327	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM	6/2016	6/2019	649.00	620.03
			(-) [0/0]	(-) [649.00]	(0.00) [0]
1328	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540	10/2017	10/2017	964.17	773.03
			(-) [11/2020]	(-) [964.17]	(0.00) [0]
1329	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	2/2008	10/2011	1,673.70	3,326.93
			(-) [0/0]	(-) [1,673.70]	(0.00) [0]
1330	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING	9/2012	10/2013	511.00	492.00
			(-) [0/0]	(-) [511.00]	(0.00) [0]
1331	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A	9/2012	10/2013	511.00	2,323.04
			(-) [0/0]	(-) [511.00]	(0.00) [0]
1332	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K	8/2020	11/2020	196.23	0.00
			(-) [8/2022]	(-) [196.00]	(-0.23) [21]
1333	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS	10/2013	5/2014	278.87	0.00
			(-) [0/0]	(-) [278.87]	(0.00) [0]
1334	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O	1/1991	4/2014	376.52	0.00
			(-) [0/0]	(-) [376.52]	(0.00) [0]
1335	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I	9/2016	/	1,100.19	1,327.00
			(-) [3/2021]	(-) [1,145.31]	(45.12) [0]
1336	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (	9/2016	/	1,239.82	1,674.80
			(-) [1/2021]	(-) [1,727.66]	(487.84) [0]
1337	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV	4/2017	4/2020	894.00	810.00
			(-) [7/2021]	(-) [929.32]	(35.32) [15]
1338	TWO LANING WITH PAVED SHOULDER OF KARAUII - DHOLPUR	9/2014	9/2016	425.19	276.40
			(-)	(-)	(0.00)

			[0/0]	[425.19]	[0]
1339	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR	8/2015	/ (-) [0/0]	275.90 (-) [275.90]	289.13 (0.00) [0]
1340	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM	7/2016	10/2018 (-) [0/0]	331.46 (-) [331.46]	267.94 (0.00) [0]
1341	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGLAUR	6/2016	6/2019 (-) [9/2019]	637.18 (-) [637.18]	550.35 (0.00) [0]
1342	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGLAUR SECTION BY EXECUTING BALANCE WORK FRO	3/2020	8/2020 (-) [8/2022]	255.23 (-) [255.23]	1.66 (0.00) [24]
1343	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE - DANTOUR-JA	3/2018	/ (-) [0/0]	874.25 (-) [874.25]	886.59 (0.00) [0]
1344	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM-	2/2018	6/2018 (-) [4/2021]	370.30 (-) [370.30]	290.00 (0.00) [34]
1345	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION	2/2018	/ (-) [9/2020]	1,103.88 (-) [1,103.88]	673.70 (0.00) [0]
1346	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM-	2/2018	5/2018 (-) [6/2021]	341.79 (-) [341.79]	208.00 (0.00) [37]
1347	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING	10/2014	1/2015 (-) [0/0]	257.09 (-) [257.09]	14.18 (0.00) [0]
1348	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24	2/2015	3/2015 (-) [0/0]	383.40 (-) [383.40]	244.68 (0.00) [0]
1349	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K	10/2014	1/2015 (-) [0/0]	269.22 (-) [269.22]	33.24 (0.00) [0]
1350	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH	12/2015	6/2018 (-) [0/0]	621.43 (-) [621.43]	387.22 (0.00) [0]
1351	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR	11/2017	4/2018 (-) [3/2021]	187.82 (-) [187.82]	131.74 (0.00) [0]
	<u>SIKKIM</u>				
	<u>Railways</u>				
1352	SEVOK RANGPO, NEFR	4/2008	12/2015 (-) [0/0]	1,339.48 (-) [8,600.00]	619.18 (7,260.52) [0]
	<u>Road Transport And Highways</u>				
1353	CONSTRUCTION & UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	8/2020	4/2023 (-) [4/2023]	311.00 (-) [311.00]	0.00 (0.00) [0]
1354	CONSTRUCTION & UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	7/2020	4/2023 (-) [4/2023]	345.38 (-) [345.38]	0.00 (0.00) [0]
1355	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	1/2013	2/2013 (6/2021) [6/2021]	182.28 (369.64) [369.64]	274.07 (187.36) [100]
1356	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	4/2013	8/2013 (6/2021) [6/2021]	151.59 (370.01) [370.01]	281.74 (218.42) [94]
1357	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM.	4/2013	8/2013 (6/2021) [6/2021]	166.27 (359.92) [359.92]	243.59 (193.65) [94]

1358	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	3/2017	/ (-) [0/0]	375.80 (-) [375.80]	52.88 (0.00) [0]
1359	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	11/2017	11/2017 (-) [0/0]	290.05 (-) [290.05]	97.21 (0.00) [0]
1360	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA	4/2017	11/2017 (-) [0/0]	318.42 (-) [318.42]	66.63 (0.00) [0]
1361	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	3/2018	6/2018 (-) [0/0]	264.84 (-) [264.84]	0.00 (0.00) [0]
1362	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N	3/2019	4/2022 (-) [4/2022]	402.94 (-) [402.94]	0.00 (0.00) [0]
1363	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600	8/2020	4/2023 (-) [4/2023]	295.97 (-) [295.97]	0.00 (0.00) [0]
1364	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00	3/2020	6/2022 (-) [6/2022]	242.97 (-) [242.97]	0.00 (0.00) [0]
1365	RHENOK-RORATHANG-PAKYONG ON NH 717A	4/2017	10/2017 (-) [0/0]	388.00 (-) [447.37]	261.20 (59.37) [0]
	<u>TAMIL NADU</u>				
	<u>Atomic Energy</u>				
1366	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	3/2013	11/2020 (-) [11/2023]	39,849.00 (-) [39,849.00]	23,925.00 (0.00) [36]
1367	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	9/2003	9/2010 (9/2016) [10/2022]	3,492.00 (5,677.00) [6,840.00]	5,935.96 (3,348.00) [145]
	<u>Civil Aviation</u>				
1368	DEVELOPMENT OF TUTICORIN AIRPORT	6/2019	3/2022 (3/2022) [3/2023]	380.87 (-) [380.87]	5.99 (0.00) [12]
1369	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	6/2018	2/2022 (-) [8/2022]	2,467.00 (-) [2,467.00]	608.22 (0.00) [6]
1370	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI	8/2018	10/2021 (-) [7/2022]	951.28 (-) [951.28]	408.94 (0.00) [9]
	<u>Coal</u>				
1371	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	4/2013	6/2015 (3/2025) [3/2025]	1,458.17 (709.06) [709.06]	484.81 (-749.11) [117]
1372	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	6/2011	12/2015 (-) [2/2021]	5,907.11 (7,980.79) [7,980.79]	7,405.84 (2,073.68) [0]
	<u>Finance</u>				
1373	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	12/2015	10/2019 (-) [7/2021]	209.00 (-) [208.96]	205.72 (-0.04) [21]
1374	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI	11/2017	11/2021 (-) [11/2021]	348.77 (-) [348.77]	123.99 (0.00) [0]
	<u>Mines</u>				
1375	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU	9/2017	6/2019 (6/2021) [12/2020]	166.62 (163.17) [163.17]	135.00 (-3.45) [0]
	<u>Petroleum</u>				

1376	AUGMENTATION OF CTMPL	12/2016	11/2021 (-) [11/2021]	228.00 (-) [228.00]	140.61 (0.00) [0]
1377	BS-VI PROJECTS	9/2017	12/2019 (-) [0/0]	1,858.00 (-) [1,858.00]	1,528.75 (0.00) [0]
1378	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI	10/2020	9/2023 (-) [9/2023]	921.00 (-) [921.00]	19.14 (0.00) [0]
1379	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	12/2017	10/2020 (1/2022) [1/2022]	466.43 (-) [466.43]	207.05 (0.00) [15]
1380	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	5/2016	12/2018 (2/2022) [2/2022]	4,497.00 (6,025.00) [6,025.00]	3,681.97 (1,528.00) [38]
1381	ENNORE-TRICHY-MADURAI LPG PIPELINE	5/2013	6/2020 (-) [0/0]	711.00 (-) [711.00]	11.12 (0.00) [0]
1382	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	11/2015	3/2019 (9/2021) [9/2021]	650.82 (-) [624.35]	447.05 (-26.47) [30]
1383	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	2/2017 (8/2022) [8/2022]	678.00 (1,472.00) [1,472.00]	19.44 (794.00) [66]
1384	RE-LIQUIFIED NATURAL GAS	8/2017	8/2020 (-) [9/2021]	421.00 (-) [300.00]	241.01 (-121.00) [13]
1385	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI	10/2020	12/2023 (-) [5/2023]	1,398.00 (-) [1,398.00]	80.68 (0.00) [-7]
	<u>Power</u>				
1386	ETTAYAPURAM SOLAR 230MW	3/2020	9/2021 (-) [9/2021]	1,316.22 (-) [1,316.22]	0.00 (0.00) [0]
1387	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY	5/2017	7/2019 (4/2021) [6/2021]	186.17 (219.66) [219.66]	157.20 (33.49) [23]
	<u>Railways</u>				
1388	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING	2/1999	3/2018 (-) [0/0]	257.00 (257.00) [238.00]	153.70 (-19.00) [0]
1389	ATTIPPATTU PUTTUR	4/2008	2/2019 (-) [0/0]	151.84 (-) [527.37]	2.59 (375.53) [0]
1390	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	4/2007	/ (5/2021) [5/2021]	931.98 (-) [1,121.00]	928.75 (189.02) [-]
1391	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	4/1999	/ (-) [3/2024]	198.68 (-) [559.95]	52.50 (361.27) [-]
1392	ERODE-PALANI	4/2008	/ (-) [0/0]	288.57 (-) [1,140.00]	1.63 (851.43) [0]
1393	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	4/2006	6/2013 (6/2022) [12/2021]	495.74 (-) [734.01]	510.69 (238.27) [102]
1394	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	2/2015	3/2020 (-) [6/2022]	760.00 (-) [1,536.00]	1,233.08 (776.00) [27]
1395	MADURAI-BODINAYAKKANUR	4/2008	/ (10/2021)	164.41 (-)	375.67 (443.72)

			[9/2021]	[608.13]	[-]
1396	MANIYACHI - NAGERCOIL (102 KM) DOUBLING	2/2015	3/2022 (-) [6/2022]	1,700.00 (-) [1,305.00]	756.45 (-395.00) [3]
1397	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	9/2007	2/2019 (-) [3/2025]	724.69 (-) [2,910.84]	1,621.40 (2,186.15) [73]
1398	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM	10/2013	4/2014 (-) [12/2020]	187.26 (-) [327.00]	268.75 (139.74) [0]
1399	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	4/2013	/ (-) [0/0]	839.00 (-) [1,500.00]	0.63 (661.00) [0]
1400	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	2/1996	3/2005 (-) [9/2021]	268.87 (-) [950.00]	928.36 (681.13) [198]
1401	TIDIVANAM-NAGARI (NL)	9/2006	/ (-) [12/2025]	582.83 (-) [582.83]	239.49 (0.00) [-]
1402	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	9/2006	/ (-) [0/0]	227.40 (-) [227.40]	63.90 (0.00) [0]
1403	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	9/1995	3/2020 (-) [3/2025]	303.98 (-) [1,720.00]	701.37 (1,416.02) [60]
1404	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM)	2/2017	3/2024 (-) [3/2026]	1,567.00 (-) [1,567.00]	0.00 (0.00) [24]
	<u>Road Transport And Highways</u>				
1405	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHHTH 170 KM)	4/2012	4/2014 (-) [1/2022]	624.00 (-) [624.00]	8.56 (0.00) [93]
1406	4-LANNING OF OTTANCHATRAM BYPASS	9/2017	9/2017 (-) [0/0]	244.27 (-) [244.27]	182.00 (0.00) [0]
1407	4-LANNING OF STHIYATHOPU-CHOLOPURAM	9/2017	9/2017 (-) [7/2022]	1,227.87 (-) [1,227.87]	566.14 (0.00) [58]
1408	CONSTRUCTION OF FLYOVER FROM KM 604/252 TO 607/060 (MARTHANDAM JUNCTION) AND FROM KM 630/116 TO 631/	5/2016	1/2017 (-) [0/0]	307.70 (-) [307.70]	312.82 (0.00) [0]
1409	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT	3/2015	8/2015 (-) [0/0]	258.97 (-) [268.92]	223.10 (9.95) [0]
1410	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I-	11/2015	8/2015 (-) [0/0]	154.14 (-) [154.14]	140.64 (0.00) [0]
1411	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	6/2011	6/2013 (-) [10/2020]	600.00 (-) [600.00]	1.65 (0.00) [0]
1412	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS	3/2018	/ (-) [1/2022]	1,016.92 (-) [1,071.00]	218.47 (54.08) [-]
1413	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120	5/2015	11/2017 (-) [0/0]	1,387.11 (-) [1,387.11]	980.46 (0.00) [0]
1414	FOUR LANING OF MADURAI- CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300)	3/2018	/ (-) [12/2021]	628.71 (-) [628.71]	310.06 (0.00) [-]
1415	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM.	3/2018	/ (-)	2,065.96 (-)	0.00 (103.04)

	123+800) SECTION OF N		[0/0]	[2,169.00]	[0]
1416	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU	2/2018	/ (-) [8/2021]	1,166.26 (-) [1,296.93]	220.78 (130.67) [-]
1417	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	3/2016	7/2016 (-) [2/2021]	641.17 (-) [641.17]	394.32 (0.00) [0]
1418	FOUR LANING OF CHETTICKULAM TO NATHAM SECTION OF NH-785 FROM CHETTICKULAM (KM 7.300) TO NATHAM (KM. 3	3/2018	/ (-) [8/2021]	505.35 (-) [505.35]	243.30 (0.00) [-]
1419	FOUR LANNING OF CHOLOPURAM-THANJAVUR	8/2017	8/2017 (-) [7/2022]	1,176.37 (-) [1,176.37]	462.14 (0.00) [59]
1420	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH	2/2016	8/2018 (-) [3/2021]	707.82 (-) [707.82]	421.01 (0.00) [0]
1421	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DSIGN CHAINAGE KM 0.000 TO KM 65.	3/2017	3/2020 (-) [12/2021]	848.45 (932.23) [848.45]	222.06 (0.00) [21]
1422	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K	2/2016	7/2018 (-) [2/2021]	641.17 (-) [641.17]	395.10 (0.00) [0]
1423	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA	7/2020	12/2021 (-) [12/2021]	3,426.00 (-) [3,426.00]	0.00 (0.00) [0]
1424	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO	3/2015	7/2015 (-) [0/0]	157.18 (162.00) [162.00]	146.79 (4.82) [0]
1425	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE	12/2017	/ (-) [3/2021]	379.90 (-) [379.90]	203.77 (0.00) [0]
1426	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	9/2011	12/2013 (-) [0/0]	1,250.00 (-) [1,250.00]	1,337.11 (0.00) [0]
1427	THIRUMAYAM - MANAMADURAI SECTION	7/2014	1/2017 (-) [0/0]	401.11 (-) [401.11]	273.89 (0.00) [0]
1428	TRICHY - KARUR	3/2007	7/2008 (-) [0/0]	516.00 (-) [516.00]	886.96 (0.00) [0]
1429	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS	5/2010	5/2013 (-) [8/2021]	374.00 (-) [166.90]	54.22 (-207.10) [99]
1430	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N	3/2018	/ (-) [0/0]	633.55 (-) [482.04]	0.00 (-151.51) [0]
1431	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	6/2015	12/2017 (-) [0/0]	563.92 (-) [563.92]	93.53 (0.00) [0]
1432	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM	3/2018	6/2019 (-) [0/0]	240.38 (-) [240.38]	74.56 (0.00) [0]
1433	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE	3/2019	11/2019 (-) [0/0]	297.55 (-) [297.55]	45.52 (0.00) [0]
1434	WIDENING TO 4 LANE / 4 LANE WITH PAVED SHOULDERS WITH STRENGTHENING OF EXISTING CARRIAGEWAY IN KM 0/	1/2016	9/2016 (-) [0/0]	162.72 (-) [162.72]	136.46 (0.00) [0]
Urban Development					
1435	CHENNAI METRO RAIL LTD (PHASE 1 EXT)	6/2016	3/2018 (-)	3,770.00 (-)	3,088.12 (0.00)

			[3/2021]	[3,770.00]	[0]
1436	CHENNAI METRO RAIL LTD (PHASE 1)	2/2009	12/2015 (-) [0/0]	14,600.00 (-) [19,058.00]	16,365.87 (4,458.00) [0]
	<u>TELANGANA</u>				
	<u>Civil Aviation</u>				
1437	CO CIVIL AVIATION RESEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD	5/2020	5/2022 (-) [5/2022]	353.61 (-) [353.61]	61.13 (0.00) [0]
	<u>Coal</u>				
1438	JALAGAM VENGALA RAO OCP-II	7/2011	3/2015 (-) [3/2023]	447.06 (-) [473.22]	79.04 (26.16) [96]
1439	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1	3/2017	3/2019 (-) [3/2022]	413.84 (-) [413.84]	230.95 (0.00) [36]
1440	KAKATIYAKHANI OPENCAST-2 PROJECT	5/2015	3/2019 (-) [3/2022]	397.09 (-) [442.42]	109.25 (45.33) [36]
1441	KALYANIKHANI OPENCAST PROJECT	7/2012	7/2016 (-) [3/2022]	417.33 (-) [384.32]	131.62 (-33.01) [68]
1442	KISTARAM OCP	11/2010	3/2015 (-) [3/2022]	242.29 (-) [164.04]	129.58 (-78.25) [84]
1443	RAMAGUNDAM OC-II EXTENSION	12/2009	3/2012 (-) [3/2023]	418.97 (-) [489.62]	416.07 (70.65) [132]
1444	RCE OF INDARAM OCP(1.20 MTPA)	7/2011	3/2015 (-) [3/2022]	162.76 (-) [349.28]	251.14 (186.52) [84]
1445	RFR OF MANUGURU OC PROJECT	11/2012	3/2016 (-) [3/2021]	430.45 (-) [415.37]	193.76 (-15.08) [0]
1446	SRP OC-II EXPANSION PROJECT	11/2016	/ (-) [3/2022]	272.73 (-) [272.73]	153.75 (0.00) [-]
	<u>Health And Family Welfare</u>				
1447	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD	10/2016	3/2020 (-) [5/2021]	209.84 (-) [209.84]	136.48 (0.00) [14]
	<u>Petroleum</u>				
1448	GRASS ROOT TERMINAL AT MALKAPUR	12/2018	4/2022 (-) [8/2023]	611.00 (-) [611.00]	76.47 (0.00) [16]
	<u>Power</u>				
1449	RAMAGUNDAM FLOATING SOLAR 100 MW	6/2019	4/2021 (-) [4/2021]	401.90 (-) [401.90]	0.00 (0.00) [0]
1450	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	1/2016	11/2020 (7/2022) [7/2022]	10,598.98 (10,997.70) [10,997.70]	8,368.64 (398.72) [20]
	<u>Railways</u>				
1451	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	4/2012	3/2016 (-) [12/2021]	632.68 (-) [950.00]	810.96 (317.32) [69]
1452	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY	3/2015	3/2021 (-) [3/2021]	636.38 (-) [636.38]	581.85 (0.00) [0]
1453	MANMAD-PARBHANI-NANDED-SECUNDERABAD- GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION	4/2017	3/2022 (-)	119.73 (185.00)	7.09 (329.66)

	AVOIDANCE SYSTEM (958 K		[12/2022]	[449.39]	[9]
1454	MANOHARABAD-KOTHPALL NEW LINE(SCR)	4/2006	3/2010 (-) [3/2024]	1,160.48 (-) [1,160.48]	502.93 (0.00) [168]
1455	MANUGURU-RAMAGUNDAM	4/2013	/	1,112.00	0.92
			(-) [0/0]	(-) [2,911.84]	(1,799.84) [0]
1456	SECUNDERABAD-MAHABUBNAGAR DOUBLING	4/2015	12/2024 (-) [12/2024]	773.94 (-) [850.00]	705.50 (76.06) [0]
	<u>Road Transport And Highways</u>				
1457	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	4/2014	9/2016 (-) [0/0]	1,266.60 (-) [1,544.00]	1,446.45 (277.40) [0]
1458	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH	1/2018	5/2020 (-) [0/0]	283.15 (-) [283.15]	105.53 (0.00) [0]
1459	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES	3/2018	7/2020 (-) [0/0]	626.76 (-) [626.76]	177.70 (0.00) [0]
1460	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM	3/2015	1/2017 (-) [0/0]	153.21 (-) [153.21]	100.95 (0.00) [0]
1461	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB	3/2017	3/2017 (-) [0/0]	4,429.00 (-) [4,429.00]	0.00 (0.00) [0]
1462	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3	3/2018	/	857.62	217.06
			(-) [0/0]	(-) [857.62]	(0.00) [0]
1463	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K	3/2018	/	802.65	380.83
			(-) [0/0]	(-) [802.65]	(0.00) [0]
1464	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM	3/2018	/	950.63	557.08
			(-) [0/0]	(-) [950.63]	(0.00) [0]
1465	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO	3/2018	/	828.29	0.00
	TELANGANA/MAHARASHT		(-) [0/0]	(-) [828.29]	(0.00) [0]
1466	FOUR LANING OF YADGIRI - WARANGAL	12/2015	11/2018 (7/2019) [3/2021]	1,423.96 (-) [1,056.08]	974.60 (-367.88) [0]
1467	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365	3/2018	7/2019 (-) [0/0]	192.67 (-) [192.67]	144.28 (0.00) [0]
1468	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR	1/2017	10/2019 (-) [0/0]	605.08 (-) [605.08]	398.78 (0.00) [0]
1469	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN	2/2018	4/2020 (-) [0/0]	426.52 (-) [426.52]	388.63 (0.00) [0]
1470	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT	1/2014	3/2016 (-) [0/0]	270.00 (-) [270.00]	19.84 (0.00) [0]
1471	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT	2/2018	11/2019 (-) [0/0]	294.13 (-) [294.13]	116.69 (0.00) [0]
1472	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS	2/2018	11/2019 (-) [0/0]	220.28 (-) [220.28]	124.56 (0.00) [0]
1473	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO	3/2018	9/2020 (-)	322.81 (-)	142.01 (0.00)

	KODAD SEC		[0/0]	[322.81]	[0]
1474	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ	10/2016	3/2019 (-) [0/0]	248.83 (-) [248.83]	116.36 (0.00) [0]
1475	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON	10/2016	2/2019 (-) [0/0]	298.32 (-) [298.32]	115.53 (0.00) [0]
1476	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4	1/2018	12/2019 (-) [0/0]	230.03 (-) [230.03]	207.56 (0.00) [0]
1477	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59	2/2018	6/2020 (-) [0/0]	206.13 (-) [206.13]	171.37 (0.00) [0]
1478	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR	1/2019	/ (-) [0/0]	193.19 (-) [193.19]	61.94 (0.00) [0]
1479	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH	1/2017	10/2019 (-) [0/0]	196.52 (-) [196.52]	107.70 (0.00) [0]
1480	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI	1/2017	12/2019 (-) [0/0]	283.00 (-) [283.00]	228.79 (0.00) [0]
1481	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE	1/2017	5/2019 (-) [0/0]	244.54 (-) [244.54]	164.33 (0.00) [0]
1482	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT	1/2017	5/2019 (-) [0/0]	359.27 (-) [359.27]	293.94 (0.00) [0]
1483	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION	1/2017	5/2019 (-) [0/0]	300.00 (-) [300.00]	184.77 (0.00) [0]
	<u>TRIPURA</u>				
	<u>Civil Aviation</u>				
1484	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	9/2015	6/2019 (12/2020) [6/2021]	438.28 (-) [402.00]	366.61 (-36.28) [24]
	<u>Railways</u>				
1485	AGARTALA-AKHAURA NL	4/2012	3/2020 (-) [3/2022]	569.63 (-) [742.00]	200.28 (172.37) [24]
	<u>Road Transport And Highways</u>				
1486	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S	10/2014	3/2018 (-) [0/0]	369.00 (-) [369.00]	322.69 (0.00) [0]
1487	2-LANING FROM MANU-SIMLUNG (PKG I)	3/2020	1/2022 (-) [1/2022]	247.76 (-) [247.76]	2.60 (0.00) [0]
1488	2-LANING FROM MANU-SIMLUNG (PKG III)	6/2020	1/2022 (-) [1/2022]	347.36 (-) [347.36]	0.00 (0.00) [0]
1489	REHABILITATION & UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE SE	3/2020	7/2022 (-) [7/2022]	154.51 (-) [154.51]	0.00 (0.00) [0]
1490	REHABILITATION & UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION	6/2020	1/2022 (-) [1/2022]	277.50 (-) [277.50]	0.00 (0.00) [0]
1491	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID	3/2020	7/2022 (-) [7/2022]	178.43 (-) [178.43]	0.00 (0.00) [0]
1492	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM	1/2017	12/2022 (-)	197.67 (-)	5.75 (0.00)

	422.00 (25 K		[12/2022]	[197.67]	[0]
1493	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C	10/2016	8/2020 (-) [7/2021]	171.90 (-) [171.90]	123.81 (0.00) [11]
	Rural Development				
1494	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	3/2007	12/2015 (-) [10/2021]	149.73 (173.00) [155.66]	144.95 (5.93) [70]
1495	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016 (-) [10/2021]	202.61 (227.00) [207.12]	190.22 (4.51) [58]
1496	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	12/2016 (-) [12/2021]	175.49 (206.71) [175.49]	124.87 (0.00) [60]
	UTTAR PRADESH				
	Civil Aviation				
1497	CCS INTERNATIONAL AIRPORT , LUCKNOW	6/2018	9/2021 (-) [9/2022]	1,383.00 (-) [1,383.00]	369.66 (0.00) [12]
	Coal				
1498	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	7/2016	11/2021 (7/2022) [7/2022]	17,237.00 (-) [17,237.80]	11,574.21 (0.80) [8]
	Health And Family Welfare				
1499	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	7/2016	4/2020 (-) [7/2021]	785.00 (-) [715.06]	548.39 (-69.94) [15]
1500	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI	3/2018	/ (-) [3/2021]	268.84 (-) [268.84]	243.92 (0.00) [0]
	Human Resource Development				
1501	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR	11/2017	3/2020 (-) [6/2021]	171.72 (-) [171.72]	53.94 (0.00) [15]
	Petroleum				
1502	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A	3/2018	8/2022 (-) [8/2022]	676.00 (-) [676.00]	433.41 (0.00) [0]
1503	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI	4/2017	4/2022 (-) [4/2022]	287.49 (345.15) [345.15]	200.77 (57.66) [0]
1504	CITY GAS DISTRIBUTION IN UP AND UK	3/2019	3/2029 (8/2029) [8/2029]	3,450.20 (-) [3,450.20]	235.43 (0.00) [5]
1505	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT	8/2018	4/2021 (-) [10/2021]	217.92 (217.92) [217.92]	89.80 (0.00) [6]
1506	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY	8/2017	8/2020 (11/2021) [11/2021]	255.40 (-) [255.40]	64.34 (0.00) [15]
1507	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL	12/2017	12/2021 (-) [12/2021]	1,524.06 (-) [1,524.06]	785.64 (0.00) [0]
1508	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR	8/2017	8/2021 (-) [11/2021]	318.80 (-) [318.80]	147.52 (0.00) [3]
	Power				
1509	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP	12/2018	9/2020 (-) [1/2021]	587.44 (-) [587.44]	463.48 (0.00) [0]
1510	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP	3/2019	11/2020	349.00	226.00

			(-) [4/2021]	(-) [349.00]	(0.00) [5]
1511	DEVIKOT SOLAR 150MW	1/2020	9/2021 (1/2022) [1/2022]	798.24 (-) [798.24]	34.64 (0.00) [4]
1512	DEVIKOT SOLAR 90MW	3/2020	9/2021 (1/2022) [1/2022]	501.29 (-) [501.29]	118.11 (0.00) [4]
1513	KHURJA SUPER THERMAL POWER PROJECT	3/2019	9/2023 (-) [8/2024]	11,089.42 (-) [11,089.42]	1,767.11 (0.00) [11]
1514	MUNPL-MEJA TPP - JV (2X660 MW)	4/2012	2/2017 (-) [1/2021]	9,750.89 (-) [12,176.28]	11,130.00 (2,425.39) [0]
1515	NOKHRA	3/2020	9/2021 (1/2022) [1/2022]	1,722.14 (-) [1,722.14]	132.85 (0.00) [4]
1516	TANDA TPP STAGE-II (2X660 MW)	9/2014	7/2019 (3/2021) [3/2021]	9,188.98 (-) [9,842.02]	7,391.78 (653.04) [0]
	<u>Railways</u>				
1517	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP	3/2013	/	307.00	0.00
			(-) [0/0]	(-) [1,409.09]	(1,102.09) [0]
1518	AUNRIHAR - JAUNPUR PATCH DOUBLING .	4/2016	1/2022 (-) [3/2022]	600.00 (-) [366.71]	117.64 (-233.29) [2]
1519	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI.	4/2016	1/2022 (-) [3/2025]	1,900.00 (-) [1,277.06]	0.00 (-622.94) [38]
1520	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	3/2012	12/2020 (-) [12/2022]	1,183.25 (-) [1,825.00]	1,411.49 (641.75) [24]
1521	BURHWAL - GONDA - 3RD RUNNING LINE.	4/2016	/	602.50	40.34
			(-) [12/2023]	(-) [714.34]	(111.84) [-]
1522	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	2/2008	3/2012 (-) [0/0]	171.10 (-) [275.08]	141.55 (103.98) [0]
1523	ETAH - KASGANJ - NEW LINE	4/2017	4/2017 (-) [4/2022]	276.90 (-) [276.90]	0.00 (0.00) [60]
1524	ETAWAH-MAINPURI (NL),NCR	4/1997	12/2008 (-) [0/0]	120.00 (-) [346.00]	345.51 (226.00) [0]
1525	GHAZIPUR - AUNRIHAR (40 KM)	4/2014	/	182.92	0.00
			(-) [0/0]	(-) [197.73]	(14.81) [0]
1526	INDARA - DOHRIGHAT GAUGE CONVERSION.	4/2016	4/2016 (-) [12/2021]	213.00 (-) [213.35]	12.86 (0.35) [68]
1527	JHANSI BINA DOUBLING	9/2016	3/2021 (-) [0/0]	2,001.00 (-) [2,001.00]	809.66 (0.00) [0]
1528	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING	3/2018	3/2023 (-) [3/2023]	4,329.53 (-) [4,329.53]	33.37 (0.00) [0]
1529	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP	3/2013	/	643.00	0.00
			(-) [0/0]	(-) [644.00]	(1.00) [0]
1530	KARAILA ROAD - SHAKTINAGAR DOUBLING	8/2015	3/2019	528.57	179.78

			(-) [3/2022]	(-) [528.57]	(0.00) [36]
1531	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	4/2011	3/2019 (-) [6/2022]	927.01 (-) [1,400.00]	1,331.76 (472.99) [39]
1532	MATHURA-JHANSI-3RD LINE (273.80 KM)	6/2016	12/2023 (-) [12/2023]	3,677.76 (-) [3,677.76]	446.65 (0.00) [0]
1533	MATHURA-PLWAL 4TH LINE (80KM)	4/2015	3/2020 (-) [0/0]	668.70 (668.00) [680.00]	330.00 (11.30) [0]
1534	MAU-GHAZIPUR-TARIGHAT NEW LINE	4/2015	3/2023 (-) [12/2024]	1,765.92 (-) [1,765.92]	887.48 (0.00) [21]
1535	NANPARA - NEPALGANJ GAUGE CONVERSION.	4/2017	4/2017 (-) [10/2022]	150.00 (-) [150.00]	0.00 (0.00) [66]
1536	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE	4/2017	1/2018 (-) [0/0]	1,343.00 (-) [1,476.15]	0.00 (133.15) [0]
1537	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION	4/2017	4/2017 (-) [3/2021]	622.50 (427.00) [426.74]	506.36 (-195.76) [0]
1538	RAMNA - SINGRAULI DOUBLING	8/2015	3/2020 (-) [3/2024]	2,436.21 (-) [2,436.21]	1,138.31 (0.00) [48]
1539	ROSA-SITAPUR CANTT-BURHWAL DOUBLING	3/2015	3/2022 (-) [3/2022]	1,295.42 (-) [1,295.42]	1,111.50 (0.00) [0]
1540	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING.	4/2016	12/2019 (-) [4/2021]	1,177.96 (-) [1,028.95]	172.26 (-149.01) [16]
1541	UNCHAHAR-AMETHI	4/2012	/ (-) [3/2023]	1,229.00 (-) [1,265.00]	103.72 (36.00) [-]
1542	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	4/2015	3/2022 (-) [12/2024]	943.60 (-) [1,000.00]	688.03 (56.40) [33]
	Road Transport And Highways				
1543	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125	9/2015	9/2016 (-) [0/0]	368.73 (-) [368.73]	239.04 (0.00) [0]
1544	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE	11/2010	3/2017 (-) [0/0]	305.49 (-) [305.49]	0.00 (0.00) [0]
1545	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232	4/2014	1/2016 (12/2020) [12/2020]	351.34 (417.68) [417.68]	433.68 (66.34) [0]
1546	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI	4/2014	1/2016 (1/2020) [1/2020]	495.78 (627.93) [627.93]	633.24 (132.15) [0]
1547	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	7/2012	1/2014 (12/2020) [12/2020]	291.36 (469.31) [469.31]	459.07 (177.95) [0]
1548	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500	8/2016	4/2019 (-) [0/0]	2,016.00 (-) [2,016.00]	1,996.00 (0.00) [0]
1549	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C	3/2018	/ (-) [0/0]	1,120.57 (-) [1,332.00]	1,118.92 (211.43) [0]
1550	4-LANING OF GAGALHERI- SAHARANPUR-	3/2016	/	1,668.00	946.08

	YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (		(-) [0/0]	(-) [1,668.00]	(0.00) [0]
1551	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I)	12/2015	6/2016 (-) [0/0]	611.65 (-) [611.65]	728.24 (0.00) [0]
1552	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00	3/2016	/ (-) [0/0]	1,408.00 (-) [1,408.00]	442.70 (0.00) [0]
1553	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00	3/2016	/ (-) [0/0]	1,737.00 (-) [1,737.00]	1,159.07 (0.00) [0]
1554	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR)	3/2016	/ (-) [0/0]	1,404.50 (-) [1,404.50]	2,977.58 (0.00) [0]
1555	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	3/2016	4/2019 (-) [0/0]	1,587.49 (-) [2,982.00]	276.87 (1,394.51) [0]
1556	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPU	3/2016	/ (-) [0/0]	1,396.74 (-) [1,396.74]	227.26 (0.00) [0]
1557	6 LANING OF AGRA - ETAWAH BYPASS	7/2015	1/2019 (-) [0/0]	1,657.20 (-) [1,657.20]	2,345.00 (0.00) [0]
1558	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	3/2017	3/2020 (-) [0/0]	2,064.99 (-) [2,447.00]	2,357.84 (382.01) [0]
1559	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN	12/2017	/ (-) [0/0]	207.00 (-) [207.00]	43.23 (0.00) [0]
1560	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020	3/2016	4/2019 (-) [0/0]	676.73 (-) [676.73]	977.26 (0.00) [0]
1561	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA	2/2018	/ (-) [0/0]	972.77 (-) [972.77]	494.71 (0.00) [0]
1562	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T	12/2016	/ (-) [0/0]	534.55 (-) [531.00]	433.62 (-3.55) [0]
1563	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O	12/2017	/ (-) [0/0]	305.00 (-) [305.00]	0.00 (0.00) [0]
1564	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO	3/2018	/ (-) [12/2021]	1,117.84 (-) [1,117.84]	0.00 (0.00) [-]
1565	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650	1/2017	/ (-) [0/0]	450.68 (-) [450.68]	397.62 (0.00) [0]
1566	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B	1/2014	3/2016 (-) [0/0]	282.41 (-) [282.41]	155.53 (0.00) [0]
1567	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM	1/2016	6/2019 (-) [0/0]	1,081.57 (-) [1,057.60]	596.79 (-23.97) [0]
1568	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM	12/2017	/ (-) [0/0]	1,232.21 (-) [1,087.00]	1,059.17 (-145.21) [0]
1569	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO	3/2017	3/2020 (-) [0/0]	1,989.00 (-) [1,989.00]	756.92 (0.00) [0]
1570	ETAWAH CHAKERI	3/2013	9/2015 (-)	1,573.00 (-)	2,093.25 (0.00)

			[0/0]	[1,573.00]	[0]
1571	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP	2/2018	/ (-) [0/0]	670.50 (-) [670.50]	75.10 (0.00) [0]
1572	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS	3/2018	/ (-) [0/0]	809.07 (-) [809.07]	517.66 (0.00) [0]
1573	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR.	3/2018	/ (-) [0/0]	925.40 (-) [1,197.00]	1,011.70 (271.60) [0]
1574	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II)	12/2015	6/2018 (-) [0/0]	667.00 (-) [667.00]	549.07 (0.00) [0]
1575	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III)	6/2016	7/2018 (-) [0/0]	667.00 (-) [667.00]	464.05 (0.00) [0]
1576	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I)	1/2016	6/2018 (-) [0/0]	1,027.53 (-) [1,027.53]	601.13 (0.00) [0]
1577	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II)	1/2016	6/2018 (-) [0/0]	815.28 (-) [815.28]	520.89 (0.00) [0]
1578	FOUR LANING OF VARANASI BYPASS	5/2015	5/2017 (-) [0/0]	261.09 (-) [261.09]	240.96 (0.00) [0]
1579	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J)	3/2018	8/2020 (-) [3/2021]	288.30 (-) [288.30]	153.66 (0.00) [0]
1580	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2	3/2017	3/2020 (-) [0/0]	1,373.28 (-) [1,373.28]	974.57 (0.00) [0]
1581	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	3/2017	3/2020 (-) [0/0]	1,184.71 (-) [1,310.00]	1,039.23 (125.29) [0]
1582	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791	3/2016	4/2019 (-) [0/0]	899.00 (-) [899.00]	641.51 (0.00) [0]
1583	GHAZIABAD-ALIGARH NH-91	2/2011	8/2013 (-) [0/0]	1,141.00 (-) [1,141.00]	1,715.42 (0.00) [0]
1584	IMPROVEMENT AND UP-GRADATION OF EXISITING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T	11/2018	/ (-) [0/0]	281.45 (-) [281.45]	0.00 (0.00) [0]
1585	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 KM	11/2018	12/2020 (-) [6/2021]	281.45 (-) [281.45]	72.05 (0.00) [6]
1586	MEERUT-BULANDSHAHR	1/2016	/ (-) [0/0]	683.24 (-) [987.94]	867.27 (304.70) [0]
1587	R AND U FROM KM 385.00 TO KM 420.000 TO 2- LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404	12/2016	10/2019 (-) [4/2020]	209.10 (-) [209.10]	201.70 (0.00) [0]
1588	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS	11/2016	/ (-) [9/2021]	326.99 (327.00) [326.99]	105.89 (0.00) [-]
1589	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS	3/2016	9/2020 (-) [5/2021]	296.50 (-) [296.50]	199.95 (0.00) [8]
1590	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU	3/2018	/ (-) [0/0]	1,025.80 (-) [677.07]	222.94 (-348.73) [0]

1591	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA	3/2018	/ (-) [0/0]	1,115.28 (-) [770.04]	332.69 (-345.24) [0]
1592	REHABILITATION AND UPGRADATION OF ALLAHABAD - MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2-	10/2016	2/2019 (-) [0/0]	239.63 (-) [239.63]	212.53 (0.00) [0]
1593	REHABILITATION AND UPGRADATION OF BARAICH - SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA	3/2016	12/2019 (-) [0/0]	388.83 (-) [388.83]	304.70 (0.00) [0]
1594	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750	3/2018	4/2020 (-) [4/2021]	263.89 (-) [242.05]	188.43 (-21.84) [12]
1595	REHABILITATION AND UPGRADATION OF HARPALPUR - SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE	3/2016	11/2019 (-) [2/2021]	208.50 (-) [208.50]	165.82 (0.00) [0]
1596	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH	10/2013	3/2017 (-) [4/2021]	445.89 (653.00) [653.29]	754.40 (207.40) [49]
1597	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F	3/2016	1/2020 (-) [0/0]	599.34 (-) [599.34]	492.15 (0.00) [0]
1598	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF	3/2018	2/2020 (-) [1/2021]	185.18 (-) [185.18]	124.59 (0.00) [0]
1599	REHABILITATION AND UPGRADATION OF TULSIPUR - BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730	3/2016	5/2019 (-) [3/2021]	249.50 (-) [249.50]	221.17 (0.00) [0]
1600	REHABILITATION AND UPGRADATION OF ALLAHABAD - MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT	10/2016	3/2020 (-) [3/2021]	218.90 (-) [218.90]	145.28 (0.00) [0]
1601	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230	3/2018	/ (-) [0/0]	306.59 (-) [306.59]	0.00 (0.00) [0]
1602	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P	11/2016	9/2019 (-) [0/0]	215.16 (215.00) [215.16]	160.61 (0.00) [0]
1603	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH	3/2016	1/2020 (-) [3/2021]	240.30 (240.00) [240.30]	210.10 (0.00) [0]
1604	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA	10/2016	3/2020 (-) [0/0]	218.94 (219.00) [218.94]	120.69 (0.00) [0]
1605	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO	10/2016	10/2018 (-) [0/0]	176.94 (177.00) [176.94]	141.11 (0.00) [0]
1606	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO	7/2016	10/2019 (-) [3/2021]	208.88 (-) [208.88]	175.79 (0.00) [0]
1607	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270	10/2013	3/2017 (-) [0/0]	445.89 (-) [653.29]	464.05 (207.40) [0]
1608	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14	11/2017	1/2019 (-) [0/0]	2,159.00 (-) [2,159.00]	1,363.84 (0.00) [0]
1609	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA	3/2018	/ (-) [0/0]	2,140.93 (-) [2,140.93]	1,344.09 (0.00) [0]
1610	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN	10/2020	3/2023 (-) [3/2023]	724.60 (-) [724.60]	0.00 (0.00) [0]
1611	VARANASI RING ROAD PKG - I	1/2018	/	450.77	0.00

			(-) [0/0]	(-) [450.77]	(0.00) [0]
1612	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH	5/2013	8/2015 (-) [1/2021]	164.54 (165.00) [164.54]	141.33 (0.00) [0]
1613	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE	5/2013	8/2015 (-) [0/0]	164.54 (-) [164.54]	128.54 (0.00) [0]
	<u>Steel</u>				
1614	FORGED WHEEL PLANT	4/2014	9/2018 (6/2021) [6/2021]	1,682.85 (-) [1,682.85]	1,564.62 (0.00) [33]
	<u>Urban Development</u>				
1615	AGRA METRO RAIL PROJECT	5/2019	3/2024 (-) [3/2024]	8,379.62 (-) [8,379.62]	0.00 (0.00) [0]
1616	KANPUR METRO RAIL PROJECT	5/2019	3/2024 (-) [3/2024]	11,076.48 (-) [11,076.48]	0.00 (0.00) [0]
1617	LUCKNOW METRO RAIL CORPORATION LTD	1/2016	3/2019 (-) [0/0]	6,928.00 (6,928.00) [6,928.00]	2,536.77 (0.00) [0]
	<u>Water Resources</u>				
1618	FARRUKHABAD I AND D AND STP WORKS HAM	10/2017	3/2022 (-) [3/2022]	213.62 (261.12) [261.12]	0.00 (47.50) [0]
1619	INTEGRATED PROJECT FOR DEVELOPMENT OF STPS IN ALLAHABAD ALONG WITH EXISTING ASSETS	3/2018	9/2021 (-) [9/2021]	904.00 (-) [904.00]	136.55 (0.00) [0]
1620	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH	1/2019	10/2021 (-) [10/2021]	206.05 (-) [206.05]	29.26 (0.00) [0]
1621	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH	1/2019	12/2021 (-) [12/2021]	231.79 (-) [234.03]	0.00 (2.24) [0]
1622	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH	3/2019	8/2021 (-) [8/2021]	271.39 (-) [271.39]	0.00 (0.00) [0]
1623	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH	3/2019	7/2021 (-) [6/2022]	298.12 (213.91) [213.91]	0.00 (-84.21) [11]
1624	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA	5/2017	9/2021 (-) [9/2021]	767.59 (-) [767.59]	76.71 (0.00) [0]
1625	MATHURA SEWERAGE SCHEME	12/2017	12/2020 (-) [5/2021]	460.45 (-) [460.45]	216.89 (0.00) [5]
1626	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA	2/2017	11/2019 (-) [3/2021]	161.31 (-) [161.31]	91.38 (0.00) [0]
1627	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH	2/2019	6/2022 (-) [6/2022]	681.78 (-) [690.71]	0.00 (8.93) [0]
1628	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA	2/2011	12/2019 (-) [1/2021]	279.91 (330.05) [330.05]	244.84 (50.14) [0]
1629	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR	10/2016	8/2020 (3/2021) [0/0]	370.40 (430.49) [430.49]	376.22 (60.09) [0]
1630	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS	3/2018	9/2021 (-)	967.23 (-)	40.59 (0.00)

			[9/2021]	[967.23]	[0]
	<u>UTTARAKHAND</u>				
	<u>Civil Aviation</u>				
1631	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN	7/2018	9/2020 (-) [12/2021]	456.86 (-) [456.86]	286.85 (0.00) [15]
	<u>Petroleum</u>				
1632	SITARGANJ LPG PROJECT	2/2017	2/2020 (6/2021) [6/2021]	160.10 (-) [160.10]	93.54 (0.00) [16]
	<u>Power</u>				
1633	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	7/2012	8/2017 (-) [0/0]	1,527.00 (-) [1,801.07]	149.21 (274.07) [0]
1634	NAITWAR MORI HEP	10/2017	12/2021 (-) [12/2021]	648.33 (-) [947.89]	577.17 (299.56) [0]
1635	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	3/2013 (12/2021) [12/2022]	2,978.48 (5,867.38) [5,867.38]	4,913.02 (2,888.90) [117]
1636	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	8/2008	6/2013 (-) [12/2023]	2,491.58 (-) [3,860.35]	2,223.06 (1,368.77) [126]
	<u>Railways</u>				
1637	HARIDWAR-LAKSAR	4/2012	/ (-) [0/0]	219.83 (-) [346.63]	204.53 (126.80) [0]
1638	KICHHA-KHATIMA (NL) - NER	4/2003	/ (-) [0/0]	142.45 (-) [228.40]	0.15 (85.95) [0]
1639	RISHIKESH - KARNAPRAYAG NEW LINE	4/2011	12/2024 (-) [3/2025]	16,216.00 (-) [22,716.11]	2,997.71 (6,500.11) [3]
	<u>Road Transport And Highways</u>				
1640	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI	3/2018	6/2018 (-) [0/0]	403.36 (-) [403.36]	99.65 (0.00) [0]
1641	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA	3/2018	5/2018 (-) [0/0]	417.24 (-) [417.24]	112.62 (0.00) [0]
1642	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	11/2012	7/2018 (-) [0/0]	605.84 (-) [722.46]	722.46 (116.62) [0]
1643	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900	3/2016	/ (-) [0/0]	1,443.00 (-) [1,443.00]	1,246.85 (0.00) [0]
1644	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399	3/2018	5/2018 (-) [0/0]	274.31 (-) [274.31]	29.13 (0.00) [0]
1645	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK)	3/2018	7/2018 (-) [0/0]	1,383.78 (-) [1,383.78]	148.70 (0.00) [0]
1646	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN	5/2018	5/2020 (-) [0/0]	248.00 (-) [248.00]	0.00 (0.00) [0]
1647	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88	3/2016	/ (-) [0/0]	720.00 (-) [720.00]	348.16 (0.00) [0]
1648	HARIDWAR DEHRADUN APPROVED LENGTH 69	11/2011	10/2013 (-) [0/0]	478.51 (-) [478.00]	315.11 (-0.51) [0]

1649	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG	11/2017	11/2019 (-) [0/0]	232.81 (-) [232.81]	59.44 (0.00) [0]
1650	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION	11/2017	11/2019 (-) [0/0]	283.51 (-) [283.51]	126.38 (0.00) [0]
1651	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	12/2017	12/2019 (-) [0/0]	257.34 (-) [257.34]	62.79 (0.00) [0]
1652	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	6/2017	6/2019 (-) [0/0]	282.08 (-) [282.08]	77.05 (0.00) [0]
1653	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	12/2017	12/2019 (-) [0/0]	200.34 (-) [200.34]	31.00 (0.00) [0]
1654	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR	2/2018	2/2020 (-) [0/0]	418.88 (-) [418.88]	88.00 (0.00) [0]
1655	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	11/2017	11/2019 (-) [0/0]	266.52 (-) [266.52]	144.27 (0.00) [0]
1656	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER	8/2016	12/2017 (-) [0/0]	234.88 (-) [208.89]	118.26 (-25.99) [0]
1657	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K	2/2018	/ (-) [0/0]	293.68 (-) [293.68]	11.57 (0.00) [0]
1658	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00	3/2018	/ (-) [0/0]	460.73 (-) [461.00]	0.00 (0.27) [0]
1659	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00	12/2017	12/2019 (-) [0/0]	248.22 (-) [248.22]	57.20 (0.00) [0]
	<u>Urban Development</u>				
1660	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOB LA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	12/2013 (-) [0/0]	114.26 (266.00) [266.00]	0.00 (151.74) [0]
	<u>Water Resources</u>				
1661	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH	3/2017	11/2019 (3/2021) [0/0]	158.00 (-) [158.00]	79.00 (0.00) [0]
1662	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI	3/2017	8/2019 (-) [0/0]	273.37 (-) [273.37]	80.45 (0.00) [0]
	<u>WEST BENGAL</u>				
	<u>Civil Aviation</u>				
1663	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA	1/2019	11/2021 (10/2022) [10/2022]	389.71 (-) [389.71]	140.62 (0.00) [11]
1664	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	1/2016	3/2020 (12/2021) [12/2021]	458.00 (-) [458.00]	135.60 (0.00) [21]
	<u>Coal</u>				
1665	2.0 MTPA BHOJUDIH NLW WASHERY	12/2015	3/2017 (-) [3/2022]	304.13 (341.22) [341.22]	40.84 (37.09) [60]
1666	EXPANSION PR OF JHANJRA UG(5.00 MTY)	11/2015	3/2022 (3/2029) [3/2029]	1,210.12 (-) [1,210.12]	26.05 (0.00) [84]
1667	NAKRAKONDA KUMARDIH B OCP	8/2018	3/2029 (-)	502.68 (-)	12.62 (0.00)

			[3/2029]	[502.68]	[0]
1668	PARASEA- BELBAID REORGANISATION UG MINE	7/2019	3/2027 (-) [3/2027]	826.42 (-) [826.42]	0.03 (0.00) [0]
1669	RANIGANJ MASTER PLAN	8/2009	8/2019 (-) [0/0]	2,661.73 (-) [5,146.48]	621.70 (2,484.75) [0]
1670	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT	4/2020	3/2025 (-) [3/2025]	483.65 (-) [483.65]	1.82 (0.00) [0]
1671	SIDULI MINE (OC AND UG)	5/2018	3/2026 (-) [3/2026]	535.18 (-) [535.18]	1.39 (0.00) [0]
1672	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	8/2012	3/2018 (-) [10/2021]	1,055.05 (-) [1,055.05]	669.82 (0.00) [43]
1673	TILABONI UG MINE	2/2019	3/2027 (-) [3/2027]	916.62 (-) [916.62]	0.61 (0.00) [0]
	<u>Health And Family Welfare</u>				
1674	CNCI KOLKATA WEST BENGAL	8/2016	9/2018 (-) [5/2019]	244.00 (-) [248.00]	224.92 (4.00) [0]
1675	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	5/2017 (-) [7/2019]	168.90 (-) [191.20]	169.51 (22.30) [0]
1676	HOSPITAL AND TEACHING- AIIMS KALYANI	4/2018	/ (-) [6/2021]	651.99 (-) [651.99]	503.55 (0.00) [-]
1677	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	8/2017	3/2019 (-) [6/2021]	355.15 (-) [355.15]	298.76 (0.00) [27]
	<u>Home Affairs</u>				
1678	NSG AT KOLKATA	10/2014	4/2018 (12/2021) [12/2021]	162.88 (238.00) [238.00]	171.19 (75.12) [44]
	<u>Human Resource Development</u>				
1679	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED	3/2020	6/2020 (-) [0/0]	193.83 (-) [193.83]	0.45 (0.00) [0]
	<u>Petroleum</u>				
1680	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL	3/2018	9/2022 (-) [3/2022]	3,712.00 (-) [3,696.00]	1,995.95 (-16.00) [-6]
1681	CITY GAS DISTRIBUTION IN WEST BENGAL	3/2019	3/2031 (8/2029) [8/2029]	5,830.20 (-) [5,830.20]	93.97 (0.00) [-19]
1682	DURGAPUR-HALDIA PIPELINE PROJECT	3/2017	12/2020 (12/2021) [12/2021]	1,740.00 (-) [1,740.00]	764.50 (0.00) [12]
1683	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY	6/2020	1/2023 (-) [1/2023]	1,019.00 (-) [1,019.00]	58.94 (0.00) [0]
1684	KHARAGPUR LPG BOTTLING PLANT	4/2017	4/2020 (10/2021) [10/2021]	163.02 (-) [163.02]	101.52 (0.00) [18]
	<u>Power</u>				
1685	DURGAPUR PP-III (2X20 MW) - NSPCL	12/2016	11/2018 (-) [7/2021]	529.68 (-) [529.68]	418.49 (0.00) [32]
1686	EASTERN REGION STRENGTHENING SCHEME-XV	4/2016	4/2018	454.11	343.81

			(3/2021) [5/2021]	(-) [454.11]	(0.00) [37]
1687	RAMMAM-III HEPP (3X40 MW)	9/2014	9/2019 (12/2024) [12/2024]	1,381.84 (-) [1,381.54]	668.04 (-0.30) [63]
	<u>Railways</u>				
1688	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	4/1998	3/2003 (-) [3/2030]	1,027.40 (1,966.70) [2,373.00]	485.04 (1,345.60) [324]
1689	BARDHAMAN-KATWA (GC)	4/2007	12/2010 (-) [3/2025]	1,106.62 (-) [1,091.59]	990.33 (-15.03) [171]
1690	BAZAR SAU -AZIMGANJ JN. DOUBLING	4/2012	/ (-) [3/2022]	255.64 (-) [272.20]	261.26 (16.56) [-]
1691	BOWAICHANDI-ARAMBAGH	4/2010	/ (-) [3/2025]	267.37 (-) [620.00]	40.99 (352.63) [-]
1692	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR	4/2009	/ (-) [3/2025]	573.78 (-) [268.52]	0.03 (-305.26) [-]
1693	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	3/2013	3/2016 (-) [6/2021]	4,874.58 (-) [8,574.97]	5,892.72 (3,700.39) [63]
1694	HOWRAH-AMTA-CHAMPADANGA NL (SER)	4/1974	3/2007 (3/2007) [0/0]	393.46 (154.30) [1,026.00]	182.49 (632.54) [0]
1695	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	4/2010	/ (-) [0/0]	221.42 (-) [380.00]	38.20 (158.58) [0]
1696	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	4/1983	3/2019 (-) [0/0]	297.32 (200.34) [614.00]	275.06 (316.68) [0]
1697	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN	2/1999	4/2010 (-) [0/0]	380.60 (-) [1,090.60]	1,089.12 (710.00) [0]
1698	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM)	4/2016	12/2021 (-) [4/2021]	602.27 (-) [2,144.78]	921.83 (1,542.51) [-8]
1699	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	4/2010	3/2014 (-) [12/2025]	2,298.42 (-) [2,733.86]	40.46 (435.44) [141]
1700	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	4/2010	3/2016 (-) [3/2025]	2,913.51 (-) [4,639.00]	1,119.31 (1,725.49) [108]
1701	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP)	4/2010	3/2016 (-) [0/0]	2,397.72 (-) [2,397.72]	197.20 (0.00) [0]
1702	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	4/2010	3/2016 (-) [3/2025]	3,951.98 (-) [4,259.48]	2,734.83 (307.50) [108]
1703	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	4/2000	3/2019 (12/2009) [3/2025]	1,188.91 (-) [1,619.48]	905.06 (430.57) [72]
1704	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	3/2000	12/2006 (-) [0/0]	1,049.69 (-) [3,404.92]	3,837.57 (2,355.23) [0]
	<u>Road Transport And Highways</u>				
1705	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	12/2015	6/2018 (-) [0/0]	1,083.00 (-) [1,827.15]	2,082.19 (744.15) [0]

1706	4-LANING OF BRAHAMPORE-FARAKA	2/2011	8/2013 (-) [6/2022]	998.79 (-) [998.79]	1,878.70 (0.00) [106]
1707	4-LANING OF FARAKA-RAIGANJ	2/2011	8/2013 (-) [5/2021]	1,078.84 (-) [1,078.84]	2,295.18 (0.00) [93]
1708	6-LANING OF DHANKUNI-KHARAGPUR SECTION	4/2012	9/2014 (-) [0/0]	1,396.18 (-) [1,396.18]	2,894.94 (0.00) [0]
1709	CONSTRUCTION OF ISLAMPUR BY PASS	10/2015	/ (-) [0/0]	361.15 (-) [363.93]	272.98 (2.78) [0]
1710	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND	3/2016	8/2019 (-) [11/2022]	160.27 (213.97) [213.97]	25.64 (53.70) [39]
1711	CONSTRUCTION OF ROB –FLYOVER AT RANICHAK, HALDIA	3/2016	11/2018 (-) [0/0]	229.37 (-) [229.37]	130.72 (0.00) [0]
1712	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N	6/2016	8/2019 (-) [12/2021]	236.78 (263.26) [263.26]	65.84 (26.48) [28]
1713	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO	3/2018	10/2020 (-) [3/2021]	254.30 (254.30) [254.30]	103.21 (0.00) [0]
1714	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA	9/2016	8/2018 (-) [0/0]	767.03 (-) [767.03]	604.65 (0.00) [0]
1715	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O	8/2014	11/2017 (-) [0/0]	600.87 (720.97) [720.97]	682.36 (120.10) [0]
1716	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O	8/2014	11/2017 (-) [0/0]	823.20 (937.76) [937.76]	807.99 (114.56) [0]
1717	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA)	3/2018	/ (-) [7/2021]	1,261.98 (-) [1,952.20]	934.06 (690.22) [-]
1718	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7	4/2014	8/2017 (1/2020) [2/2020]	279.70 (398.52) [398.52]	322.91 (118.82) [0]
1719	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN	1/2017	9/2019 (11/2020) [5/2021]	396.86 (396.86) [396.86]	242.98 (0.00) [20]
1720	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL	1/1991	3/2018 (-) [0/0]	322.00 (-) [322.00]	56.41 (0.00) [0]
1721	SIX-LANING OF BARWA ADDA-PANAGARH	4/2014	/ (-) [0/0]	1,665.00 (-) [2,360.65]	4,472.01 (695.65) [0]
1722	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10	3/2017	11/2019 (-) [0/0]	202.69 (202.69) [202.69]	144.89 (0.00) [0]
1723	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4	2/2018	11/2020 (4/2020) [4/2021]	218.70 (218.70) [218.70]	104.09 (0.00) [5]
1724	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19.	2/2018	9/2020 (-) [12/2021]	426.18 (426.18) [426.18]	249.01 (0.00) [15]
	<u>Steel</u>				
1725	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E	12/2018	9/2020 (3/2021) [9/2021]	263.36 (-) [263.36]	215.38 (0.00) [12]

	<u>Water Resources</u>				
1726	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR	2/2014	12/2019 (5/2021) [5/2021]	274.76 (-) [274.76]	202.13 (0.00) [17]
1727	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS	1/2019	4/2022 (-) [4/2022]	384.96 (-) [384.96]	0.00 (0.00) [0]
1728	I AND D AND STP WORKS AT BURDWAN WEST BENGAL	12/2018	4/2022 (-) [4/2022]	234.31 (-) [234.31]	0.00 (0.00) [0]
1729	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS	3/2018	6/2022 (-) [6/2022]	165.16 (-) [165.16]	0.00 (0.00) [0]
1730	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH	5/2018	2/2022 (-) [10/2022]	160.00 (154.73) [154.73]	0.00 (-5.27) [8]
1731	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPURL	3/2019	4/2022 (-) [4/2022]	287.53 (-) [287.53]	0.00 (0.00) [0]
1732	INTERCEPTION AND DIVERSION WITH STP AT BALLY	10/2017	12/2021 (-) [12/2021]	164.93 (-) [164.93]	0.00 (0.00) [0]
1733	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA	5/2018	2/2022 (-) [6/2022]	198.43 (224.69) [224.69]	0.00 (26.26) [4]
1734	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA	8/2017	9/2022 (-) [9/2022]	307.12 (-) [307.12]	0.00 (0.00) [0]
1735	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI	1/2018	12/2021 (-) [12/2021]	172.10 (-) [172.10]	0.00 (0.00) [0]
1736	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH	8/2017	12/2021 (-) [12/2021]	185.22 (-) [185.22]	0.00 (0.00) [0]
1737	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE	12/2014	4/2020 (-) [3/2021]	272.32 (-) [272.32]	220.73 (0.00) [0]
	Total			22,33,409.53 (6,39,362.44) [26,71,440.77]	13,16,032.62 (4,38,031.24)
