

केन्द्रीय क्षेत्र की परियोजनाओं
CENTRAL SECTOR PROJECTS
(150 करोड़ रु. और अधिक लागत वाली)
(150 Crore and above)
के संबंध में/ ON

322वीं फ्लैश रिपोर्ट/ 322nd FLASH REPORT

अगस्त, 2012/ August, 2012



भारत सरकार / Government of India
सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय
Ministry of Statistics and Programme Implementation
आधारी संरचना और परियोजना प्रबोधन प्रभाग
Infrastructure and Project Monitoring Division
सरदार पटेल भवन, संसद मार्ग
Sardar Patel Bhavan, Sansad Marg
नई दिल्ली / New Delhi-110001
वेबसाइट / Website- www.cspm.gov.in

Contents

Executive Summary in Hindi	1 -5
Executive Summary in English	6-11
Month wise list of completed projects Costing Rs. 1000 Crore and Above During 2010-11	2-14
Summary of Projects	15-28
Trend and Graphical Analysis of Projects	29-41
Sector wise analysis of projects	42-42
List of All Ongoing Projects	43-70
Sector wise Graph	71-83
ANNEXURE	84-84
Central Sector Projects	85-85
List of Projects Having Expenditure More than cost	86-91
List of Projects Ahead of Schedule	92-92
List of Projects with out Original date of Commissioning	93-95
List of Projects with out date of Commissioning	96-100
List of On schedule Projects	101-109
List of Projects without Milestones	110-127
List of Delayed Projects w.r.t Original and Revised	128-148
List of Projects Having cost overrun w.r.t original	149-158
List of Projects Having cost and time overrun w.r.t original	159-163
Abbreviations	164-165

कार्यकारी सारांश

अगस्त, 2012 की फ्लैश रिपोर्ट में 150 करोड़ रुपए तथा अधिक लागत वाली केन्द्रीय क्षेत्र की 560 आधारी संरचना परियोजनाओं की स्थिति दी गई है। अगस्त, 2012 के दौरान 5 परियोजनाओं (विद्युत में 3 परियोजनाएं इस्पात और सड़क परिवहन तथा राजमार्गक्षेत्र प्रत्येक में 1 परियोजना) के पूरा होने की सूचना दी गई है।

2. संदर्भाधीन माह के दौरान, 560 परियोजनाओं में से 260 परियोजनाओं में अद्यतन अनुसूची की तुलना में विलंब हुआ तथा 69 परियोजनाओं में पिछले माह में सूचित की गई समापन की तारीख की तुलना में अतिरिक्त विलंब की सूचना दी गई है। इन 69 परियोजनाओं में से, 30 परियोजनाएं 1000 करोड़ रु. और अधिक लागत वाली बड़ी परियोजनाएं हैं। सड़क परिवहन और राजमार्ग, कोयला, नागर विमानन, विद्युत, पेट्रोलियम, पोत परिवहन तथा पत्तन, इस्पात तथा दूरसंचार क्षेत्रों से संबंधित परियोजनाओं के संबंध में 1 से 23 महीनों तक का अतिरिक्त विलंब हुआ है।

क्र.सं.	क्षेत्र	निगरानी की जा रही परियोजनाएं	अद्यतन अनुसूची की तुलना में विलंबित परियोजनाएं	रिपोर्ट वाले माह के दौरान अतिरिक्त विलंबित परियोजनाएं	अतिरिक्त विलंबित (बड़ी परियोजनाएं)
1.	रेलवे	127	39	0	0
2.	सड़क परिवहन एवं राजमार्ग	146	83	16	4
3.	विद्युत	94	43	19	12
4.	पेट्रोलियम	69	36	18	9
5.	कोयला	51	22	1	1
6.	दूरसंचार	15	10	8	0
7.	पोत परिवहन एवं पत्तन	19	6	2	1
8.	इस्पात	17	10	4	3
9.	उर्वरक	5	2	0	0
10.	नागर विमानन	6	2	1	0
11.	परमाणु ऊर्जा	5	5	0	0
12.	शहरी विकास	4	1	0	0
13.	जल संसाधन	1	1	0	0
14.	पेट्रोरसायन	1	0	0	0
कुल		560	260	69	30

3. 560 परियोजनाओं के कार्यान्वयन की कुल मूल लागत लगभग 765702.99 करोड़ रुपए है तथा उनके पूरा होने की अनुमानित लागत 883467.92 करोड़ रुपए होनेकी संभावना है जो 117764.93 करोड़ रुपए (मूल लागत का 15.4%) की समग्र लागत वृद्धि को दर्शाती है । अगस्त, 2012 तक इन परियोजनाओं पर वहन किया गया व्यय 412178.56 करोड़ रुपए है जो परियोजनाओं की अनुमानित लागत का 46.7% है ।

4. 560 परियोजनाओं में से, 5 परियोजनाएं अनुसूची से पहले चल रही हैं, 225 अनुसूची के अनुसार तथा 260 परियोजनाएं नवीनतम अनुसूची की तुलना में विलंबित हैं । तथापि, विलंबित परियोजनाओं की संख्या 272 तक और बढ़ जाती है यदि समापन की मूल अनुसूची के आधार पर गणना की जाती है । इसके अलावा, 38 परियोजनाएं शुरू करने की किसी अनुसूची/तारीख के बिना स्वीकृत की गई हैं तथा 32 परियोजनाओं के संबंध में न तो शुरू करने का वर्ष और न परियोजना के अनुमानित रूप से पूरा होने का समय सूचित किया गया है । 260 विलंबित परियोजनाओं में से, 85 परियोजनाओं में 1 से 12 माह तक का विलंब हुआ, 47 परियोजनाओं में 13 से 24 महीने तक का विलंब हुआ, 96 परियोजनाओं में 25 से 60 माह तक का विलंब हुआ तथा 32 परियोजनाओं में 61 माह तथा अधिक का विलंब हुआ ।

5. विभिन्न परियोजना कार्यान्वयन एजेंसियों द्वारा यथा सूचित समय वृद्धि के लिए संक्षिप्त कारणों में भूमि अधिग्रहण, नगरपालिका की अनुमति में विलंब, सामग्री की खरीद में विलंब, कार्य सौंपने में विलंब, टीजी संस्थापन आरंभ करने में विलंब, कार्यों के दायरे में वृद्धि, स्थान में परिवर्तन, सौंपे गए कार्यों को निरस्त करना, जनशक्ति की कमी, मौसम की स्थिति, विक्रेता संबंधी मामले, आरओयू/आरओडब्ल्यू समस्याएं तथा ठेकेदारों द्वारा घटिया संघटन आदि शामिल हैं ।

6. मंत्रालय द्वारा ऑनलाइन कम्प्यूटराइज्ड मॉनीटरिंग सिस्टम (ओसीएमएस) में विभिन्न आधारी संरचना परियोजनाओं की पीईआरटी चार्टों से तैयार किए गए लक्ष्यों के प्रबोधन की परिकल्पना की गई है । परियोजना प्राधिकारियों से नियमित रूप से अनुरोध किया गया है कि वे बेहतर मॉनीटरिंग सुनिश्चित करने के लिए प्रत्येक परियोजना के लिए लक्ष्यों की सूची की प्रविष्टि करें । तथापि, सभी एजेंसियां लक्ष्यों की सूची प्रदान नहीं कर रही हैं, यह भी पाया गया है कि परियोजना एजेंसियां बहुत सी परियोजनाओं के लिए लागत के संशोधित अनुमान तथा शुरू होने की सूची नहीं बता रही हैं जिनसे यह संकेत मिलता है कि समय/लागत वृद्धि के आंकड़े कम करके बताए गए हैं ।

7. विलंब/अतिरिक्त विलंब का क्षेत्र-वार ब्यौरा निम्नानुसार है:-

(i) पोत परिवहन एवं पत्तन क्षेत्र में, 19 परियोजनाओं में से 6 परियोजनाएं विलंबित हैं। माह के दौरान 2 परियोजनाओं के संबंध में 1 और 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। इन दोनों परियोजनाओं में से, 'पुथु में एलएनजी रीगैसीफिकेशन टर्मिनल की स्थापना, पोर्ट ट्रस्ट' नामक परियोजना बड़ी परियोजना है जिसके संबंध में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है तथा दूसरी परियोजना अर्थात '3060 डीडब्ल्यूडीक्षमता के दो जहाजोंकीखरीद, नौवहन' के संबंध में एक माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों ने कोई विशिष्ट कारण नहीं बताए हैं।

(ii) नागरविमान क्षेत्र में, 6 परियोजनाओं में से 2 परियोजनाएं विलंबित हैं। माह के दौरान, 'नई अंतर्राष्ट्रीय टर्मिनल बिल्डिंगका निर्माण, एएआई, गोवा' नामक परियोजना के संबंध में स्थल-परिवर्तन के कारण 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है।

(iii) कोयला क्षेत्र में, 51 परियोजनाओंमें से 22 परियोजनाएं विलंबित हैं। माह के दौरान, 'नेवेली न्यू थर्मल पावर प्रोजेक्ट (2X500 बड़ीवॉट), एनएलसी' नामक बड़ी परियोजना के संबंध में 20 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। तथापि, इन परियोजनाओं में विलंब के लिए परियोजनाओं प्राधिकारियों ने कोई विशिष्ट कारण नहीं बताए हैं।

(iv) दूरसंचार क्षेत्र में, 15 परियोजनाओं में से 10 परियोजनाएं विलंबित हैं। माह के दौरान 8 परियोजनाओं के संबंध में 2-6 माह की अवधि के अतिरिक्त विलंब की सूचना मिली है। एक परियोजना के संबंध में 2 माह के अतिरिक्त विलंब की सूचना मिली है। '390 हजार लाइन(2जी) एवं 130 हजार लाइन (3जी) का जीएसएम उपस्कर, बीएसएनएल', 799000 लाइन (2जी) एवं 101000 लाइन (3जी) का जीएसएम उपस्कर, बीएसएनएल' तथा 'असम टेलीकॉम सर्किल फेज-VI 2जी एवं 3जी, बीएसएनएल' नामक परियोजनाओं के संबंध में, नगरपालिका संबंधी अनुमति प्राप्त करने में विलंब होने के कारण क्रमश 3 माह, 3 माह और 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। '283000 लाइन (2जी) एवं 75000 लाइन का जीएसएम उपस्कर, बीएसएनएल' और 'टर्नकी आधार पर बीएसएनएल में ईआरपी कार्यान्वयन, बीएसएनएल' के संबंध में, क्रमश: प्रतिकूल मौसम संबंधी स्थिति के कारण सामग्री के परिवहन में विलंबहोने तथा विक्रेता-संबंधी मुद्दे के कारण प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 'मैसेजिंग स्टोरेजके एनआईबी-II की परियोजना-III, बीएसएनएल' एवं 'एनआईबी परियोजना क्षमता विस्तार, बीएसएनएल' के संबंध में, क्रमश: ब्रॉडबैंड सेवाओं के अंतरण से संबंधित मुद्दे तथा लाइन में डाटा सेंटर इन्फ्रास्ट्रक्चर तैयार न होने के कारण प्रत्येक में 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है।

(V) **पेट्रोलियम क्षेत्र** में, 69 परियोजनाओं में से 36 परियोजनाएं विलंबित हैं। माह के दौरान, 18 परियोजनाओं के संबंध में 1-12 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है। इन 18 परियोजनाओं में से 9 बड़ी परियोजनाएं हैं। 2 परियोजनाओं के संबंध में 1-1 माह, 2 परियोजनाओं के संबंध में 2-2 माह, दो परियोजनाओं के संबंध में 3 और 4 माह, 3 परियोजनाओं के संबंध में प्रत्येक में 5 माह तथा 5 परियोजनाओं के संबंध में प्रत्येक में 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 'कोनाबन जीजीएस का उन्नयन एवं पाइपलाइन ग्रिड परियोजना, ओएनजीसी' नामक परियोजना के संबंध में आरओयू मामले के कारण 7 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। '12 ऑफशोर सप्लाई वेसल (ओएसवी) का निर्माण, ओएनजीसी' तथा 'कोच्चि कूटनाड बंगलौर मंगलौर पाइपलाइन पीएच-II, गेल' के संबंध में क्रमशः कुशल श्रमिकों की कमी एवं आरओयू समस्या के कारण प्रत्येक में 8 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 'क्लस्टर-7 फील्ड का विकास, ओएनजीसी' परियोजना के संबंध में कार्य सौंपने में हुए विलंब के कारण 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है।

(VI) **विद्युत क्षेत्र** में, 94 परियोजनाओं में से 43 परियोजनाएं विलंबित हैं। माह के दौरान 19 परियोजनाओं के संबंध में 1-15 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है। इन 19 परियोजनाओं में से 12 बड़ी परियोजनाएं हैं। 4 परियोजनाओं के संबंध में प्रत्येक में 1 माह, 2 परियोजनाओं के संबंध में 2 माह, 2 परियोजनाओं के संबंध में 3 माह, 2 परियोजनाओं के संबंध में 5 माह तथा 2 परियोजनाओं के संबंध में 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 'बोंगाईगांव थर्मल पावर परियोजना, एनटीपीसी' एवं 'उत्तरी क्षेत्र सिस्टम सुदृढीकरण स्कीम-XV, पीजीसीआईएल' नामक परियोजनाओं के संबंध में क्रमशः टीजी इरेक्शन आरंभ होने में विलंब तथा भूमि अधिग्रहण में विलंब होने के कारण 7 और 9 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 'जेन.से विद्युत अंतरण हेतु पारेषण प्रणाली, पीजीसीआईएल' के संबंध में भूमि अधिग्रहण के कारण 10 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, 'कोलडैम एचईपी, एनटीपीसी के संबंध में प्राइमरी कॉन्क्रीटिंग पूरा होने में विलंब के कारण 12 माह के अतिरिक्त विलंब की सूचना मिली है, 'तुईरियाल पनबिजली परियोजना (60 बड़ीवाट), नीपको' के संबंध में जनशक्ति की कमी के कारण 13 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, 'बीएआरएच एसटीपीपी स्टेज-I (3X660 बड़ीवाट) एनटीपीसी' तथा 'तपोवन-विष्णुगढ़ एचईपी (4X130 बड़ीवाट), एनटीपीसी' के संबंध में क्रमशः इकाई 1 और 2 कंडेंसर इरेक्शन में परिणामी विलंब तथा ठेकेदार द्वारा कार्य न किए जाने के कारण अवार्ड-टर्मिनेशन की वजह से प्रत्येक में 15 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है।

(vii) **इस्पात क्षेत्र** में, 17 परियोजनाओं में से 10 परियोजनाएं विलंबित हैं । माह के दौरान 4 परियोजनाओं के संबंध में 2 से 5 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है । इन 4 परियोजनाओं में से 3 बड़ी परियोजनाएं हैं । 'कोक ओवन बैटरी नं.4 फेज-II, आरआईएनएल' नामक परियोजना के संबंध में बोली लगाने वालों द्वारा एनआईटी में दिलचस्पी न लेने के कारण 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, 'भिलाई इस्पात संयंत्रका विस्तार, सेल' और 'दुर्गापुर इस्पात संयंत्रका विस्तार, सेल' परियोजनाओं के संबंध में क्रमशः स्ट्रक्चरल पैकेजों की मात्राओं में वृद्धि एवं कार्यों के क्षेत्र-विस्तार के कारण प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । 'एक्सपेंशन ऑफ आरआईएनएल/वीएसपी फ्रॉम 3 एमटीपीवाई-6.3 एमटीपीवाई ऑफ लिक्विड स्टील, आरआईएनएल' नामक परियोजना के संबंध में ठेकेदार द्वारा खराब संघटन तथा इरेक्शन उपस्कर की कमी के कारण 5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।

(viii) **सड़क परिवहन एवं राजमार्ग क्षेत्र** में, 146 परियोजनाओं में से 83 परियोजनाएं विलंबित हैं । माह के दौरान 16 परियोजनाओं के संबंध में 1-23 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है । इन 16 परियोजनाओं में से 4 बड़ी परियोजनाएं हैं । 2 परियोजनाओं के संबंध में एक-एक माह, 7 परियोजनाओं के संबंध में प्रत्येक में 2 माह तथा 2 परियोजनाओं के संबंध में 3 और 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । 'पठानकोट-भोगपुर, कि.मी.26-कि.मी.70, एनएस-38 एनएच-1ए, एनएचएआई' परियोजना से 7 माह, 'काज़ीगुंड-बनिहाल कि.मी.220 से कि.मी.188, एनएचएआई' और नशरी चननी, एनएचएआई' से प्रत्येक में 11 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । 'पुणे-शोलापुर पीकेजी1, एनएचएआई' और 'लखनादौन से मध्य प्रदेश/महाराष्ट्र सीमा (एनएस-1/बीओटी/एमपी-2), एनएच-7, एनएचएआई' परियोजनाओं से क्रमशः 12 और 23 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । परियोजना एजेंसी ने इन परियोजनाओं में विलंब के लिए किसी विशेष कारण का उल्लेख नहीं किया है । तथापि, इन परियोजनाओं में विलंब के सामान्य कारणों में भूमि अधिग्रहण में देरी, वन एवं पर्यावरण संबंधी अनापत्ति, जन सुविधाओं के अंतरण संबंधी समस्या, ठेकेदार का खराब निष्पादन, आदि शामिल हैं ।

8. दिनांक 01.09.2012 तक की स्थिति के अनुसार विभिन्न क्षेत्रों में 150 करोड़ रुपए और उससे अधिक लागत वाली परियोजनाओं की स्थिति रिपोर्ट में दर्शायी गई है ।



(टी.सी.ए. अनंत)

सचिव,

सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय

EXECUTIVE SUMMARY

The Flash Report for August, 2012 contains information on the status of the 560 Central Sector Infrastructure Projects, costing ₹150 Crores and above. During, August, 2012, 5 projects (3 projects in Power, 1 project each in Steel and Road Transport & Highways Sector) have reported completion.

During the reference month, out of 560 projects 260 projects are delayed w.r.t latest schedule and 69 projects have reported additional delays, vis-à-vis the date of completion reported in the previous month. Out of these 69 projects, 30 are Mega Projects costing ₹ 1000 Crore and above. The additional delays are in the range of 1 to 23 months, in respect of projects relating to Road Transport and Highways, Coal, Civil Aviation, Power, Petroleum, Shipping & Ports, Steel and Telecommunication Sectors.

S. No.	Sector	Projects on monitor	Delayed Projects w.r.t latest Scheduled	Additionally delayed during the month under report	Additionally delayed (Mega Projects)
1.	RAILWAYS	127	39	0	0
2.	ROAD TRANSPORT & HIGHWAYS	146	83	16	4
3.	POWER	94	43	19	12
4.	PETROLEUM	69	36	18	9
5.	COAL	51	22	1	1
6.	TELECOMMUNICATION	15	10	8	0
7.	SHIPPING & PORTS	19	6	2	1
8.	STEEL	17	10	4	3
9.	FERTILISERS	5	2	0	0
10.	CIVIL AVIATION	6	2	1	0
11.	ATOMIC ENERGY	5	5	0	0
12.	URBAN DEVELOPMENT	4	1	0	0
13.	WATER RESOURCES	1	1	0	0
14.	PETROCHEMICALS	1	0	0	0
Total		560	260	69	30

3. The total original cost of implementation of the 560 projects was about ₹ 7,65,702.99 Crores and their anticipated completion cost is likely to be ₹ 8,83,467.92 Crores, which reflects an overall cost overrun of ₹ 1,17,764.93 Crores (15.4% of original cost). The expenditure incurred on these projects till August, 2012 is ₹ 4,12,178.56 Crores, which is 46.7 % of the anticipated cost of the projects.

4. Out of the 560 projects, 5 projects are ahead of schedule, 225 are on schedule and 260 projects are delayed with respect to latest schedule. However, the numbers of delayed projects further increases to 272 if delay is calculated on the basis of original scheduled of completion. Further, 38 projects have been sanctioned without any commissioning schedule/date and for 32 projects neither the year of commissioning nor the tentative gestation period of the projects have been reported. Out of 260 delayed projects, 85 projects had overall delay in the range of 1 to 12 months, 47 projects had a delay in the range of 13 to 24 months, 96 projects had a delay in the range of 25 to 60 months and 32 projects had a delay of 61 months and above.

5. The brief reasons for time overruns as reported by various projects implementing agencies are land acquisition, delay in municipal permission, delay in procurement of material, delay in award of work, delay in TG erection start, increase in scope of works, change in location, termination of award, shortage of manpower, weather condition, vendor related issue, ROU/ROW problem and poor mobilization by the contractor, etc.

6. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones drawn from the PERT Charts of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are providing the list of milestones. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedule for many projects, which suggest that time/cost overrun figures are underreported.

7. **The Sector-wise details of delays/additional delays are as under:-**

i) In the **Shipping and Ports sector**, out of 19 projects, 6 projects are delayed. During the month 2 projects have reported additional delays of 1 and 2 months. Out of these two, one projects namely 'Setting up of LNG Regasification Terminal at Puthu, Port Trust' is Mega project which has reported additional delay of 2 months and other project namely 'Acquisition of Two nos. of 3060 DWT, Shipping' has reported additional delay of 1 month. However, no specific reasons have been reported by the project authorities for delay in these projects.

ii) In the **Civil Aviation sector**, out of 6 projects, 2 projects are delayed. During the month the project namely 'Construction of New International Terminal Building, AAI', Goa, has reported additional delays of 4 months due to change in location.

iii) In the **Coal sector**, out of 51 projects, 22 projects are delayed. During the month one Mega Project, namely Neyveli New Thermal Power Project (2x500 MW), NLC' has reported additional delays of 20 months. However, no specific reasons have been reported by the project authorities for delay in this project.

iv) In the **Telecommunications sector**, out of 15 projects, 10 projects are delayed. During the month 8 projects have reported additional delays in the range of 2-6 months. One project has reported additional delays of 2 months. The projects 'GSM Equipment of 390K Lines(2G) and 130K Lines(3G), BSNL', 'GSM Equipment of 799000 Lines (2G) 101000 Lines (3G), BSNL' and 'Assam Telecom Circle Phase-V.I 2G & 3G, BSNL' have reported additional delay of 3 months, 3 months & 6 months respectively due to delay in obtaining the municipal permission, GSM Equipment of 283000 Lines (2G) and 75000 Lines, BSNL' and 'ERP Implementation in BSNL on Turnkey Basis, BSNL' have reported additional delays of 3 months each due to delay in transportation of material because of bad weather condition and vendor related issue respectively. The projects 'Project-III of NIB-II of Messaging Storage, BSNL' and 'NIB Project Capacity Expansion, BSNL' have reported additional delays of 4 months each due to issue related to migration of broadband services and non-readiness of data center infrastructure in line respectively.

v) In the **Petroleum Sector**, out of 69 projects, 36 projects are delayed. During the month 18 projects have reported additional delays in the range of 1-12 months. Out of these 18, nine are Mega Projects. Two projects have reported additional delays of 1 month each, two projects have reported additional delay of 2 months each, one project each has reported additional delay of 3 and 4 months, three projects have reported additional delay of 5 months each and five projects have reported additional delay of 6 months each. The project Upgradation of Konaban GGS and Pipeline Grid Project, ONGC' has reported additional delay of 7 months due to ROU issue, 'Construction of 12 Offshore Supply Vessels (OSV), ONGC' and 'Kochi Kootanad Banglore Manglore Pipeline PH-II, GAIL' have reported additional delay of 8 months each due to shortage of skilled manpower and ROU problem respectively. The project 'Development of Cluster-7 Fields, ONGC' has reported additional delay of 12 months due to delay in award of work.

vi) In the **Power Sector**, out of 94 projects, 43 projects are delayed. During the month 19 projects have reported additional delays in the range of 1-15 months. Out of these 19, twelve are Mega Projects. Four projects have reported additional delays of one month each, two projects have reported additional delays of 2 months, two projects have reported additional delays of 3 months, two projects have reported additional delays of 5 months and two projects have reported additional delays of 6 months. The project 'Bongaigaon Thermal Power Project, NTPC' and 'Northern Region System Strengthening Scheme-XV, PGCIL' have reported additional delays of 7 and 9 months due to delay in TG erection start and delay in land acquisition respectively, 'Transmission System for Transfer of Power from Gen., PGCIL' has reported additional delays of 10 months due to land acquisition, 'Koldam HEP, NTPC' has reported additional delays of 12 months due to delay in completion of primary concreting, 'Tuirial Hydro Electric Project (60MW), NEEPCO' has reported additional delays of 13 months due to shortage of manpower, 'BARH STPP Stage- I (3X660MW) NTPC' and 'Tapovan-Vishnugad HEP (4x130MW), NTPC' have reported additional delays of 15 months each due to consequential delay of unit 1 & 2 condenser erection and termination of award due to non-performance of contractor respectively.

vii) In **Steel sector**, out of 17 projects, 10 projects are delayed. During the month 4 projects have reported additional delays in the range of 2-5 months. Out of these 4, three are Mega Projects. The projects 'Coke Oven Battery No. 4 Phase-II, RINL' has reported additional delay of 2 months due to non-response to the NIT by bidders, 'Expansion of Bhilai Steel Plant, SAIL' and 'Expansion of Durgapur Steel Plant, SAIL' have reported additional delay of 3 months each due to increase in quantities in structural packages and increase in scope of works respectively. The project 'Expansion of RINL/VSP from 3 MTPY-6.3 MTPY of Liquid Steel, RINL' has reported additional delay of 5 months due to poor mobilization by the contractor and lack of erection equipment.

viii) In the **Road Transport and Highways Sector**, out of 146 projects, 83 projects are delayed. During the month 16 projects have reported additional delays in the range of 1-23 months. Out of these 16, four are Mega Projects. Two projects have reported additional delays of one month each, 7 projects have reported additional delays of 2 months each and one project each has reported additional delay of 3 and 4 months. The projects 'Pathankot-Bhogpur, KM.26-KM.70, NS-38 NH-1A, NHAI' has reported additional delays of 7 months, 'Quazigund-Banihal KM.220 to KM.188, NHAI' and 'Nashri Chanani, NHAI' have reported additional delays of 11 months each. The projects 'Pune-Sholapur PKG1, NHAI' and 'Lakhnadon to MP/MH Border (NS-1/BOT/MP-2), NH-7, NHAI' have reported additional delays 12 and 23 months respectively. The project agency has not mentioned any specific reason for delay in these projects. However, general reasons for delay in these projects are delay in land acquisition, forest & environment clearance, utility shifting problem, poor performance of contractor, etc.

8. The status as on 01.09.2012 in respect of projects costing ₹ 150 Crores and above in the various sectors is indicated in the Report.

(T.C.A. Anant)
Secretary,
Ministry of Statistics and Programme Implementation

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Additional Delayed
1	Road Transport & Highways	146	16
2	Railways	127	0
3	Power	94	19
4	Petroleum	69	18
5	Coal	51	1
6	Shipping & Ports	19	2
7	Steel	17	4
8	Telecommunications	15	8
9	Civil Aviation	6	1
10	Atomic Energy	5	0
11	Fertilisers	5	0
12	Urban Development	4	0
13	Petrochemicals	1	0
14	Water Resources	1	0
	Total	560	69

ANNEXURE-I

Month wise List of Completed Project Costing Rs. 150 Crore and above during 2012-2013

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
April, 2012				
<u>Power</u>				
1	KOTESHWAR HEP (THDC) (TEHRI HYDRO DEVELOPMENT CORPORATION LIMITED) - [180100184]	1,301.56	04/2005	2635.39
2	WESTERN REGION STRENGTHENING SCHEME-X (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000049]	664.96	02/2012	362.1
<u>Road Transport & Highways</u>				
3	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000085]	600.24	10/2009	805.1
4	Bijapur-Hungund Section (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000137]	748.00	-	N.A.
<u>Shipping & Ports</u>				
5	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C (SHIPPING corp. of india) - [N25000033]	1,061.96	03/2012	1284.15
6	ACQUISITION OF TWO NOS OF 120 B.P BY 077 & 078 (AH (SHIPPING corp. of india) - [N25000058]	241.50	09/2011	262.8
<u>Telecommunications</u>				
7	GSM EQUIPMENT OF 700K LINES (2G) AND 150K LINES (3G) (BHARAT SANCHAR NIGAM LIMITED) - [N26000046]	277.34	03/2009	308.13
8	GSM equipment of 1867000 Lines (2G) 383000 lines 3 (BHARAT SANCHAR NIGAM LIMITED) - [N26000089]	868.00	08/2009	558.78
May, 2012				
<u>Fertilisers</u>				
9	THAL AMMONIA REVAMP PROJECT (RASHTRIYA CHEMICAL & FERTILISER LIMITED) - [N08000003]	488.75	04/2012	307.89
<u>Petroleum</u>				
10	DIESEL HYDRO TREATMENT PROJECT, BRPL DHALIGAON (BONGAIGAON REFINERY PETROLEUM LIMITED) - [N16000009]	1,431.91	09/2009	1596.8
<u>Power</u>				

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2012-2013**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
11	MAUDA TRANSMISSION SYSTEM(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000084]	469.38	10/2012	224.6
	<u>Railways</u>			
12	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL)(RAIL VIKAS NIGAM LTD.) - [N22000034]	230.73	03/2009	328.83
13	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSION(RAIL VIKAS NIGAM LTD.) - [N22000081]	200.80	-	323.35
	<u>Road Transport & Highways</u>			
14	HALDIA PORT (PORT CONNECTIVITY) (NH-41)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240104196]	273.00	03/2005	475.55
15	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000103]	441.00	-	958.09
	<u>Shipping & Ports</u>			
16	MARINE LIQUID TERMINALS(ENNORE TANK TERMINAL PVT.LTD.) - [N25000054]	196.25	06/2006	250.77
17	DEVELOPMENT OF COAL TERMINAL(ENNORE PORT LTD.) - [N25000055]	399.13	08/2010	351.08
18	DEVELOPMENT OF IRON ORE TERMINAL(ENNORE PORT LTD.) - [N25000056]	370.00	08/2010	351.61
	June,2012			
	<u>Steel</u>			
19	INSTALLATION OF 700TPD AIR SEPARATION UNIT-4 AT O(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000023]	232.93	05/2011	191.83
	<u>Power</u>			
20	CHAMERA,STAGE-III (NHPC)(NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [180100241]	1,405.63	08/2010	1842.24
21	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.)(POWER GRID CORPORATION OF INDIA LIMITED) - [180100260]	3,779.46	09/2009	N.A.
22	IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000082]	215.86	06/2012	179.7
	<u>Railways</u>			
23	MUZAFFARPUR-SITAMARHI(NL),ECR(EAST CENTRAL RAILWAYS) - [220100194]	100.00	03/2012	466.7
24	SRIGANGANAGAR-SARUPSAR (GC), NWR(NORTH WESTERN RAILWAY) - [220100313]	143.92	03/2011	235.37
	<u>Road Transport & Highways</u>			
25	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106292]	227.00	12/2008	383.2

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2012-2013**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
26	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHA)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106300]	225.00	10/2008	261.9
	July,2012			
	<u>Power</u>			
27	WESTERN REGION SYSTEM STRENGTHENING SCHEME- XI(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000051]	409.50	02/2012	123.5
	<u>Railways</u>			
28	RAJPIPLA-ANKELASHWAR, WR (GC)(WESTERN RAILWAY) - [N22000096]	196.97	03/2011	218.66
	August,2012			
	<u>Steel</u>			
29	REBUILDING OF COKE OVEN BATTERIES No. 1 & 2 (BOKA(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000033]	500.90	-	355.21
	<u>Power</u>			
30	SIPAT STPP STAGE - I (NTPC)(NATIONAL THERMAL POWER CORPORATION) - [180100229]	8,323.39	12/2009	8230
31	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XIII(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000054]	317.69	11/2011	199.5
32	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000067]	196.10	07/2011	139.1
	<u>Road Transport & Highways</u>			
33	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106235]	193.09	03/2008	189.15


Summary of projects in the Flash Report for the month of August, 2012

I. Project Implementation - Current Status:

Number of Projects in Previous Month	560
Number of Projects completed/dropped/frozen in Previous Month	2
Number of Projects completed/dropped/frozen in Current Month	6
Number of Projects Removed From the System in Current Month	1
Number of Projects Added in Current Month	9
Number of Projects in Current Month	560


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 560 projects, 5 projects are ahead of schedule, 167 projects are on schedule and 272 projects are delayed. Of the balance, 83 projects do not have fixed dates of commissioning while 33 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

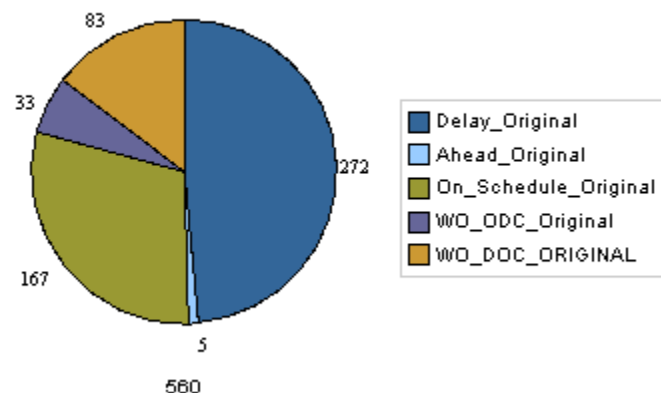

III. Investment Scenario

The Total Original cost of implementation of 560 projects when sanctioned, was of the order of Rs. 765702.99 crore but this was subsequently revised to Rs. 883467.92 crore implying a cost overrun of 15.4%. The expenditure incurred on these projects till August, 2012 is Rs. 412178.56 crore, which is 46.7% of the revised cost of the projects.

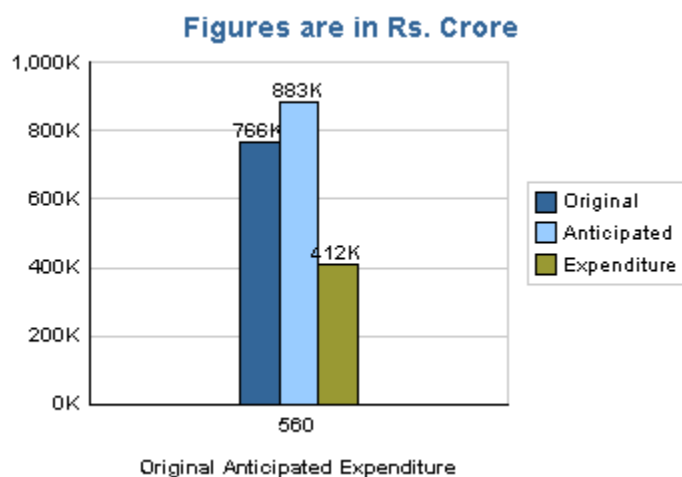

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	560
No of Projects Completed/Dropped/Frozen in Previous Month	2
No of Projects Completed/Dropped/Frozen in Current Month	6
No of Projects Removed from the System in Current Month	1
No of Projects added in Current Month	9
No of Projects in Current Month	560

II. Project status

With Respect To	Number of Projects					Total	Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C		
Original (Date)	272	5	167	33	83	560	48.57
Latest Approved (Date)	260	5	225	38	32	560	46.43

III. (A) Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	405	606,705.22	635,696.20	259,597.61	40.80	28,990.98	4.80
Latest Approved (RCE)	155	218,189.49	247,771.72	152,580.95	61.60	29,582.23	13.60
Total (RCE)	560	824,894.71	883,467.92	412,178.56	46.65	58573.21	7.10
Original Cost of All Projects							
Original Cost	560	765,702.99	883,467.92	412,178.56	46.70	117,764.93	15.40

III. (B) Delayed Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	272	397,110.20	470,464.70	275,853.84	58.60	73,354.50	18.50
Latest Approved (RCE)	260	386,134.22	426,148.73	249,823.35	58.60	40,014.51	10.40

IV. Additional Delayed Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Latest Approved	70	168,973.76	179,641.25	104,666.39	58.30	10,667.49	6.30

Extent of cost overrun in projects with respect to original schedule(Sector Wise)

S.No.	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Original	Anticipated cost	Cost overrun (%)	No .	Original cost	Anticipated cost	% Incr Base
1	Atomic Energy	5	41,548.3	47,832.3	15.1	2	16,663.0	22,947.0	37.7
2	Civil Aviation	6	5,473.6	6,063.1	10.8	2	3,750.5	4,340.0	15.7
3	Coal	51	36,056.5	37,312.3	3.5	7	8,579.5	10,433.0	21.6
4	Fertilisers	5	4,828.7	4,828.7	0.0	0	0.0	0.0	0.0
5	Steel	17	65,285.9	71,443.4	9.4	6	24,028.9	30,216.4	25.8
6	Petrochemicals	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	63.4
7	Petroleum	69	157,954.5	166,784.0	5.6	16	51,356.4	68,156.0	32.7
8	Power	94	224,936.1	238,936.5	6.2	18	41,492.2	55,492.7	33.7
9	Railways	127	64,518.7	131,959.4	104.5	107	42,495.8	112,152.1	163.9
10	Road Transport & Highways	146	92,448.7	94,027.3	1.7	11	3,324.3	5,445.2	63.8
11	Shipping & Ports	19	16,242.5	18,554.1	14.2	11	9,532.5	12,151.1	27.5
12	Telecommunications	15	6,161.0	6,101.8	-1.0	2	1,065.9	1,089.3	2.2
13	Urban Development	4	44,245.2	49,518.1	11.9	2	6,509.2	11,782.1	81.0
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		560	765,703.0	883,467.9	15.4	186	214,801.5	344,311.9	60.3

Extent of cost overrun in projects with respect to original schedule(State Wise)

S.No.	State	No. of Projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Original	Anticipated cost	Cost overrun (%)	No .	Original cost	Anticipated cost	% Incr Base
1	Andhra Pradesh	36	31,031.6	38,459.0	23.9	14	12,420.0	20,714.4	66.8
2	Arunachal Pr.	4	9,512.2	14,153.6	48.8	2	6,441.3	11,082.7	72.1
3	Assam	36	22,463.9	34,047.4	51.6	12	10,491.8	22,169.3	111.3
4	Bihar	30	26,901.2	34,657.0	28.8	13	12,343.6	20,099.4	62.8
5	Goa	1	335.6	335.6	0.0	0	0.0	0.0	0.0
6	Gujarat	22	31,111.6	31,313.5	0.6	5	2,413.7	2,885.5	19.5
7	Haryana	10	5,496.6	7,367.2	34.0	3	1,448.2	3,318.8	129.2
8	Himachal Pr.	5	13,355.6	15,414.9	15.4	3	6,781.4	8,840.8	30.4
9	J and K	10	14,927.0	22,827.6	52.9	6	7,866.5	15,767.1	100.4
10	Karnataka	24	44,634.8	52,983.8	18.7	9	8,598.8	17,354.3	101.8
11	Kerala	5	5,469.7	6,911.2	26.4	3	4,295.7	5,737.2	33.6
12	Madhya pradesh	23	16,561.5	16,856.0	1.8	3	2,027.6	2,741.5	35.2
13	Maharashtra	55	96,485.6	111,451.9	15.5	19	32,618.4	50,059.3	53.5
14	Manipur	1	727.6	4,444.0	510.8	1	727.6	4,444.0	510.8
15	Meghalaya	2	762.0	762.0	0.0	0	0.0	0.0	0.0
16	Mizoram	2	1,533.0	3,307.1	115.7	1	619.3	2,393.5	286.5
17	Nagaland	1	850.0	850.0	0.0	0	0.0	0.0	0.0
18	Orissa	30	57,409.1	61,398.9	6.9	12	32,671.6	36,661.4	12.2
19	Punjab	7	4,836.2	5,778.0	19.5	2	532.4	1,474.2	176.9
20	Rajasthan	14	26,544.1	26,138.3	-1.5	3	1,080.0	1,344.9	24.5
21	Sikkim	2	1,648.9	3,690.0	123.8	1	1,339.5	3,380.6	152.4
22	Tamil Nadu	32	51,276.0	62,055.8	21.0	14	29,143.5	39,923.4	37.0
23	Tripura	3	1,522.4	2,053.2	34.9	2	1,234.4	1,765.2	43.0
24	Uttar Pradesh	24	18,613.3	22,451.1	20.6	8	3,498.5	7,384.5	111.1
25	West Bengal	26	40,889.9	51,090.4	24.9	16	23,547.4	35,916.8	52.5
26	Delhi	5	38,572.6	38,553.0	-0.1	0	0.0	0.0	0.0
27	Chhatisgarh	24	46,715.2	47,998.3	2.7	6	1,548.3	2,831.4	82.9
28	Jharkhandd	22	14,293.6	18,275.2	27.9	6	1,897.3	6,050.7	218.9
29	Uttaranchal	3	5,619.2	6,559.6	16.7	2	2,640.7	3,581.2	35.6
30	Multi State	101	135,603.2	141,284.3	4.2	20	6,574.0	16,389.9	149.3
Total		560	765,703.0	883,467.9	15.4	186	214,801.5	344,311.9	60.3

Extent of the time overrun in projects with respect to original schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.3	47,832.3	15.1	3	36,950.0	41,049.0	3 - 51
2	Civil Aviation	6	5,473.6	6,063.1	10.8	3	2,587.6	2,970.1	7 - 27
3	Coal	51	36,056.5	37,312.3	3.5	24	20,907.9	22,115.5	12 - 60
4	Fertilisers	5	4,828.7	4,828.7	0.0	0	0.0	0.0	-
5	Steel	17	65,285.9	71,443.4	9.4	11	51,228.4	57,386.0	2 - 41
6	Petrochemicals	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
7	Petroleum	69	157,954.5	166,784.0	5.6	39	80,979.5	89,805.0	1 - 120
8	Power	94	224,936.1	238,936.5	6.2	48	125,135.9	138,523.3	3 - 99
9	Railways	127	64,518.7	131,959.4	104.5	39	23,563.1	53,465.0	1 - 216
10	Road Transport & Highways	146	92,448.7	94,027.3	1.7	84	37,210.4	39,149.0	2 - 103
11	Shipping & Ports	19	16,242.5	18,554.1	14.2	10	8,446.1	10,038.7	5 - 87
12	Telecommunications	15	6,161.0	6,101.8	-1.0	9	3,163.3	3,167.1	24 - 83
13	Urban Development	4	44,245.2	49,518.1	11.9	1	6,395.0	11,609.0	15 - 15
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	60 - 60
Total		560	765,703.0	883,467.9	15.4	272	397,110.2	470,464.7	

Extent of the time overrun in projects with respect to original schedule(State Wise)

S. No	State	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Andhra Pradesh	36	31,031.6	38,459.0	23.9	12	15,494.5	19,105.6	2 - 41
2	Arunachal Pr.	4	9,512.2	14,153.6	48.8	3	9,356.2	13,737.9	25 - 78
3	Assam	36	22,463.9	34,047.4	51.6	32	16,023.7	23,962.6	12 - 120
4	Bihar	30	26,901.2	34,657.0	28.8	14	20,578.4	26,451.2	2 - 75
5	Goa	1	335.6	335.6	0.0	1	335.6	335.6	7 - 7
6	Gujarat	22	31,111.6	31,313.5	0.6	5	13,715.4	13,885.6	9 - 24
7	Haryana	10	5,496.6	7,367.2	34.0	4	2,065.9	3,555.1	9 - 50
8	Himachal Pr.	5	13,355.6	15,414.9	15.4	5	13,355.6	15,414.9	20 - 99
9	J and K	10	14,927.0	22,827.6	52.9	9	13,826.3	21,726.9	10 - 201
10	Karnataka	24	44,634.8	52,983.8	18.7	9	22,364.3	27,349.0	7 - 98
11	Kerala	5	5,469.7	6,911.2	26.4	3	4,674.0	5,324.0	11 - 58
12	Madhya pradesh	23	16,561.5	16,856.0	1.8	15	12,669.5	12,264.0	5 - 60
13	Maharashtra	55	96,485.6	111,451.9	15.5	23	46,933.1	56,792.3	5 - 120
14	Manipur	1	727.6	4,444.0	510.8	1	727.6	4,444.0	60 - 60
15	Meghalaya	2	762.0	762.0	0.0	0	0.0	0.0	-
16	Mizoram	2	1,533.0	3,307.1	115.7	2	1,533.0	3,307.1	7 - 11
17	Nagaland	1	850.0	850.0	0.0	0	0.0	0.0	-
18	Orissa	30	57,409.1	61,398.9	6.9	11	3,545.7	3,859.0	4 - 132
19	Punjab	7	4,836.2	5,778.0	19.5	4	1,611.4	2,553.2	1 - 58
20	Rajasthan	14	26,544.1	26,138.3	-1.5	6	19,992.2	19,687.9	3 - 47
21	Sikkim	2	1,648.9	3,690.0	123.8	1	309.5	309.5	27 - 27
22	Tamil Nadu	32	51,276.0	62,055.8	21.0	11	30,528.8	36,459.4	9 - 87
23	Tripura	3	1,522.4	2,053.2	34.9	1	288.0	288.0	7 - 7
24	Uttar Pradesh	24	18,613.3	22,451.1	20.6	13	12,215.4	14,148.4	5 - 91
25	West Bengal	26	40,889.9	51,090.4	24.9	15	24,981.7	31,887.4	3 - 135
26	Delhi	5	38,572.6	38,553.0	-0.1	1	249.0	229.4	72 - 72
27	Chhatisgarh	24	46,715.2	47,998.3	2.7	7	19,008.1	19,319.4	6 - 47
28	Jharkhandd	22	14,293.6	18,275.2	27.9	10	8,767.6	9,927.4	12 - 102
29	Uttaranchal	3	5,619.2	6,559.6	16.7	2	2,640.7	3,581.2	22 - 42
30	Multi State	101	135,603.2	141,284.3	4.2	52	79,319.2	80,558.8	1 - 216
Total		560	765,703.0	883,467.9	15.4	272	397,110.2	470,464.7	

Extent of the time overrun in projects with respect to latest schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.3	47,832.3	15.1	5	41,548.3	47,832.3	3 - 51
2	Civil Aviation	6	5,473.6	6,063.1	10.8	2	2,278.1	2,660.6	7 - 17
3	Coal	51	36,056.5	37,312.3	3.5	22	18,809.8	20,436.9	12 - 60
4	Fertilisers	5	4,828.7	4,828.7	0.0	2	763.0	763.0	9 - 12
5	Steel	17	65,285.9	71,443.4	9.4	10	42,536.4	45,095.0	2 - 26
6	Petrochemicals	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
7	Petroleum	69	157,954.5	166,784.0	5.6	36	71,058.0	74,888.8	0 - 86
8	Power	94	224,936.1	238,936.5	6.2	43	116,805.9	128,254.6	3 - 99
9	Railways	127	64,518.7	131,959.4	104.5	39	15,203.5	42,805.8	0 - 216
10	Road Transport & Highways	146	92,448.7	94,027.3	1.7	83	36,930.4	38,869.0	2 - 103
11	Shipping & Ports	19	16,242.5	18,554.1	14.2	6	7,001.8	8,242.8	11 - 34
12	Telecommunications	15	6,161.0	6,101.8	-1.0	10	3,500.1	3,504.0	17 - 83
13	Urban Development	4	44,245.2	49,518.1	11.9	1	6,395.0	11,609.0	15 - 15
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	60 - 60
Total		560	765,703.0	883,467.9	15.4	260	363,373.3	426,148.7	

Extent of cost overrun in projects with respect to latest schedule

S.No.	Sector	No. of projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Latest approved	Anticipated cost	Cost overrun (%)	No .	Latest approved	Anticipated cost	% Increase Base
1	Atomic Energy	5	41,548.3	47,832.3	15.1	2	16,663.0	22,947.0	37.7
2	Civil Aviation	6	5,680.6	6,063.1	6.7	1	1,942.5	2,325.0	19.7
3	Coal	51	37,022.5	37,312.3	0.8	5	6,336.3	6,626.1	4.6
4	Fertilisers	5	4,828.7	4,828.7	0.0	0	0.0	0.0	0.0
5	Steel	17	71,161.2	71,443.4	0.4	3	598.0	910.3	52.2
6	Petrochemicals	1	8,920.0	8,920.0	0.0	0	0.0	0.0	0.0
7	Petroleum	69	171,901.1	166,784.0	-3.0	2	30,533.0	31,324.0	2.6
8	Power	94	228,743.2	238,936.5	4.5	12	34,502.4	44,695.8	29.5
9	Railways	127	93,061.6	131,959.4	41.8	74	40,117.4	79,224.2	97.5
10	Road Transport & Highways	146	92,615.2	94,027.3	1.5	11	3,324.3	5,445.2	63.8
11	Shipping & Ports	19	18,400.6	18,554.1	0.8	7	4,306.6	4,770.0	10.8
12	Telecommunications	15	6,164.9	6,101.8	-1.0	0	0.0	0.0	0.0
13	Urban Development	4	44,304.1	49,518.1	11.8	1	6,395.0	11,609.0	81.5
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		560	824,894.7	883,467.9	7.1	119	145,261.4	211,063.6	45.3

Extent of time & cost overrun in projects with respect to latest schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.29	47,832.29	15.12	0	0.00	0.00	0- 0
2	Civil Aviation	6	5,473.58	6,063.07	10.77	1	1,808.00	2,015.00	13- 13
3	Coal	51	36,056.46	37,312.25	3.48	0	0.00	0.00	0- 0
4	Fertilisers	5	4,828.66	4,828.66	0.00	0	0.00	0.00	0- 0
5	Steel	17	65,285.87	71,443.41	9.43	2	8,987.89	12,898.17	10- 41
6	Petrochemicals	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
7	Petroleum	69	157,954.47	166,783.98	5.59	12	20,971.88	35,745.22	24- 120
8	Power	94	224,936.05	238,936.53	6.22	2	2,253.45	3,986.02	0- 67
9	Railways	127	64,518.68	131,959.43	104.53	15	8,540.69	23,473.12	1- 141
10	Road Transport & Highways	146	92,448.72	94,027.34	1.71	0	0.00	0.00	0- 0
11	Shipping & Ports	19	16,242.52	18,554.09	14.23	6	6,013.42	7,487.89	5- 87
12	Telecommunications	15	6,161.00	6,101.79	-0.96	0	0.00	0.00	0- 0
13	Urban Development	4	44,245.18	49,518.08	11.92	0	0.00	0.00	0- 0
14	Water Resources	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		560	765702.99	883467.92	15.38	38	48575.33	85605.42	

Extent of time & cost overrun in projects with respect to original schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.29	47,832.29	15.12	1	13,171.00	17,270.00	51- 51
2	Civil Aviation	6	5,473.58	6,063.07	10.77	1	1,942.51	2,325.00	17- 17
3	Coal	51	36,056.46	37,312.25	3.48	4	7,617.44	9,422.79	19- 45
4	Fertilisers	5	4,828.66	4,828.66	0.00	0	0.00	0.00	0- 0
5	Steel	17	65,285.87	71,443.41	9.43	6	24,028.89	30,216.43	2- 41
6	Petrochemicals	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
7	Petroleum	69	157,954.47	166,783.98	5.59	10	19,202.27	33,652.50	24- 120
8	Power	94	224,936.05	238,936.53	6.22	16	40,474.74	53,862.08	7- 99
9	Railways	127	64,518.68	131,959.43	104.53	32	13,972.11	43,878.88	1- 216
10	Road Transport & Highways	146	92,448.72	94,027.34	1.71	11	3,324.28	5,445.20	21- 101
11	Shipping & Ports	19	16,242.52	18,554.09	14.23	7	7,365.57	8,958.14	5- 87
12	Telecommunications	15	6,161.00	6,101.79	-0.96	2	1,065.85	1,089.32	24- 42
13	Urban Development	4	44,245.18	49,518.08	11.92	1	6,395.00	11,609.00	15- 15
14	Water Resources	1	542.90	1,187.00	118.64	1	542.90	1,187.00	60- 60
Total		560	765702.99	883467.92	15.38	92	139102.56	218916.34	

V. List of projects completed/dropped/Frozen current month

(All Cost /Expenditure in Rs. crore)

			Original		Now anticipated		Final
S.no	Project	DOA	Cost	DOC	Cost	DOC	Expenditure
<u>Power</u>							
1	SIPAT STPP STAGE - I (NTPC)	12/2003	8,323.39	12/2009	8,323.39	06/2012	8,230.00
2	LOHARINAG-PAL HEP(4X150MW)	06/2006	2,895.10	11/2011	2,895.10	12/2012	.00
3	NORTHERN REGION SYSTEM STRENGHTENING SCHEME-XIII	02/2009	317.69	11/2011	317.69	08/2012	199.50
4	SYSTEM STRENGHTENING -XI IN SOUTHERN REGION	03/2009	196.10	07/2011	196.10	08/2012	139.10
<u>Road Transport & Highways</u>							
5	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00	12/2003	193.09	03/2008	166.30	07/2012	189.15
<u>Steel</u>							
6	REBUILDING OF COKE OVEN BATTERIES No. 1 & 2 (BOKA	10/2007	500.90	N.A.	500.90	02/2012	355.21

VI. List of projects added

(All Cost in Rs. crore)

S.no	Project	DOA	Original		Anticipated	
			Cost	DOC	Cost	DOC
<u>Petroleum</u>						
1	IOR of B-173A Field	1/2012	352.49	3/2014	352.49	3/2014
2	Fire water network at Uran	5/2010	171.68	6/2013	171.68	6/2013
<u>Road Transport & Highways</u>						
3	6-LANING OF DHANKUNI-KHARAGPUR SECTION	4/2012	1,396.18	9/2014	1,396.18	9/2014
4	LUCKNOW-RAIBAREILI	7/1999	635.90	7/2012	635.90	7/2012
5	KRISHNANAGAR-BERHAMPUR	2/2012	702.16	7/2014	702.16	7/2014
6	NAGPUR-WAINGANGA BRIDGE	4/2012	484.19	10/2014	484.19	10/2014
7	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	7/2012	291.36	1/2014	291.36	1/2014
<u>Steel</u>						
8	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, chattisga	7/2012	332.65	8/2014	332.65	8/2014
9	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Oddisha	1/2012	254.90	12/2014	254.90	12/2014

VII. Milestones (Cumulative due & achieved)

Total	3228
Achieved up to month	1164

VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
<u>Civil Aviation</u>							
1	Construction of New International Terminal Building AAI	335.61	335.61	05/2012	08/2012	12/2012	4
<u>Coal</u>							
2	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) NLC	5,907.11	5,907.11	12/2015	12/2015	08/2017	20
<u>Steel</u>							
3	COKE OVEN BATTERY NO. 4 PHASE-II RINL	108.00	216.68	10/2012	10/2012	12/2012	2
4	EXPANSION OF BHILAI STEEL PLANT SAIL	17,265.00	17,265.00	03/2013	06/2013	09/2013	3
5	EXPANSION OF DURGAPUR STEEL PLANT SAIL	2,875.00	2,875.00	12/2012	12/2012	03/2013	3
6	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL RINL	8,692.00	12,291.00	10/2009	10/2012	03/2013	5
<u>Petroleum</u>							
7	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-GAIL	238.68	302.00	N.A.	09/2012	10/2012	1
8	KOCHI-KOOTANAD BANGALORE-MANGALORE PIPELINE PROJEK GAIL	348.00	261.00	03/2012	08/2012	09/2012	1
9	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH ONGC	740.02	740.02	03/2010	03/2013	05/2013	2
10	MRPL Phase-III Expansion Mangalore Refin	12,412.00	12,160.26	01/2012	09/2012	11/2012	2
11	PARADIP REFINERY PROJECT IOCL	29,777.00	30,426.00	N.A.	06/2013	09/2013	3
12	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I GAIL	4,543.43	2,300.00	03/2012	08/2012	12/2012	4
13	North Tapti Gas Field Development ONGC	589.70	755.76	03/2011	10/2012	03/2013	5
14	Fluidized catalytic cracking unit(FCCU) revamp IOCL	1,000.00	1,000.00	01/2013	01/2013	06/2013	5
15	Development of SB-14 field ONGC	410.44	410.44	11/2012	05/2013	10/2013	5
16	DEV OF G1 AND GS-15 (ONGCL) ONGC	429.82	2,735.65	04/2006	12/2012	06/2013	6
17	ADDITIONAL DEV. OF D-1 FIELD ONGC	2,163.64	2,163.64	06/2012	12/2012	06/2013	6
18	Polypropylene unit Mangalore Refin	1,803.78	1,803.78	07/2012	10/2012	04/2013	6
19	Construction of 6 ETPs ONGC	302.26	240.95	09/2012	12/2012	06/2013	6


VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
20	102 MW WIND POWER PROJECT ONGC	1,106.00	820.00	06/2012	04/2013	10/2013	6
21	Up-gradation of Konaban GGS and Pipeline Grid Project ONGC	288.04	288.04	08/2012	08/2012	03/2013	7
22	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) ONGC	736.65	736.65	09/2011	12/2012	08/2013	8
23	KOCHI KOOTTANAD BANGLORE MANGLORE PIPELINE PH-II GAIL	2,915.00	2,915.00	12/2012	04/2013	12/2013	8
24	Development of Cluster-7 Fields ONGC	3,241.03	3,241.03	03/2013	04/2013	04/2014	12
<u>Power</u>							
25	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE NHPC	768.92	1,628.00	03/2007	12/2012	01/2013	1
26	URI H.E.P STAGE -II (NHPC) NHPC	1,729.29	2,083.00	11/2009	02/2013	03/2013	1
27	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP PGCIL	297.37	386.32	07/2011	10/2012	11/2012	1
28	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA PGCIL	1,347.32	1,347.32	02/2012	10/2012	11/2012	1
29	RIHAND STTP STAGE-III (2X500MW) (NTPC) NTPC	6,230.81	6,230.81	10/2012	03/2013	05/2013	2
30	System Strengthening -XII of SR PGCIL	232.34	232.34	06/2012	08/2012	10/2012	2
31	SUBANSIRI LOWER H.E.P (NHPC) NHPC	6,285.33	10,667.00	09/2010	12/2016	03/2017	3
32	EASTERN REGION STRENGTHENING SCHEME-I PGCIL	975.96	975.96	10/2009	12/2012	03/2013	3
33	PARBATI H.E.P. STAGE -III (NHPC) NHPC	2,304.56	2,716.00	10/2010	01/2013	06/2013	5
34	BARH STTP STAGE -II NTPC	7,341.04	7,341.04	08/2013	01/2014	06/2014	5
35	System Strengthening -X of SR PGCIL	276.61	276.61	04/2012	04/2012	10/2012	6
36	EASTERN REGION TRANSMISSION SYSTEM-III PGCIL	1,272.80	1,272.80	11/2012	09/2013	03/2014	6
37	BONGAIGAON THERMAL POWER PROJECT NTPC	4,375.35	4,375.35	07/2011	04/2014	11/2014	7
38	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV PGCIL	520.48	520.48	11/2011	03/2013	12/2013	9
39	Transmission system for transfer of power from Gen. PGCIL	250.03	250.03	01/2013	01/2013	11/2013	10
40	KOLDAM HEP (NTPC) NTPC	4,527.15	4,527.15	04/2009	03/2013	03/2014	12
41	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) NEEPCO	913.63	913.63	07/2014	01/2014	02/2015	13
42	BARH STTP STAGE I (3X660MW) NTPC NTPC	8,692.97	8,693.00	12/2009	12/2014	03/2016	15
43	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) NTPC	2,978.48	2,978.48	N.A.	06/2014	09/2015	15
<u>Road Transport & Highways</u>							
44	Surat- Dahisar(Six Lane) Km 263 to Km 502 NHAI	1,693.75	1,693.75	08/2011	09/2012	10/2012	1
45	Hyderabad-yadgiri N.H no-202 NHAI	388.00	388.00	05/2012	08/2012	09/2012	1
46	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) NHAI	241.00	196.65	08/2004	08/2012	10/2012	2


VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
47	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) NHAI	318.00	207.56	08/2004	08/2012	10/2012	2
48	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) NHAI	225.00	241.53	04/2004	07/2012	09/2012	2
49	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) NHAI	151.30	151.30	10/2008	08/2012	10/2012	2
50	GANJAM-ICCHAPURUM,NH-5(NHAI) NHAI	263.27	263.27	02/2004	07/2012	09/2012	2
51	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 NHAI	228.70	228.70	02/2004	07/2012	09/2012	2
52	Armur to kadloor yellareddy NHAI	390.56	390.56	02/2012	07/2012	09/2012	2
53	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA NHAI	229.91	229.91	10/2008	09/2012	12/2012	3
54	BHOPAL-SANCHI NHAI	209.00	209.00	01/2013	06/2013	10/2013	4
55	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A NHAI	284.00	359.00	05/2008	08/2012	03/2013	7
56	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 NHAI	1,987.00	1,987.00	07/2015	07/2015	06/2016	11
57	NASHRI CHANANI NHAI	2,159.00	2,159.00	06/2015	06/2015	05/2016	11
58	Pune-sholapur, pkg1 NHAI	1,110.00	1,110.00	05/2012	10/2012	10/2013	12
59	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 NHAI	263.17	263.17	09/2009	10/2012	09/2014	23
Shipping & Ports							
60	Acquisition of Two nos. of 3060 DWT SHIPP.	277.03	277.03	12/2011	08/2012	09/2012	1
61	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU PORT TRUST	3,500.00	4,150.00	01/2012	10/2012	12/2012	2
Telecommunications							
62	GSM equipment of 1625000Lines (2G) 325000 lines 3(BSNL	916.70	930.60	11/2010	09/2012	11/2012	2
63	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) BSNL	373.94	373.94	12/2008	09/2012	12/2012	3
64	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES BSNL	149.15	158.72	06/2009	09/2012	12/2012	3
65	GSM equipment of 799000Lines (2G) 101000 lines 3(G BSNL	328.13	328.12	03/2009	09/2012	12/2012	3
66	ERP implementation in BSNL on Turnkey basis BSNL	384.00	384.00	10/2010	12/2012	03/2013	3
67	PROJ.III OF NIB-II OF MESSAGING STORAGE BSNL	250.00	250.00	12/2005	07/2012	11/2012	4
68	NIB Project Capacity Expansion BSNL	175.52	175.52	12/2008	07/2012	11/2012	4
69	Assam Telecom Circle, Phase-V.I, 2G & 3G BSNL	336.81	336.81	01/2009	09/2012	03/2013	6

Trend and Graphical Analysis of All Projects

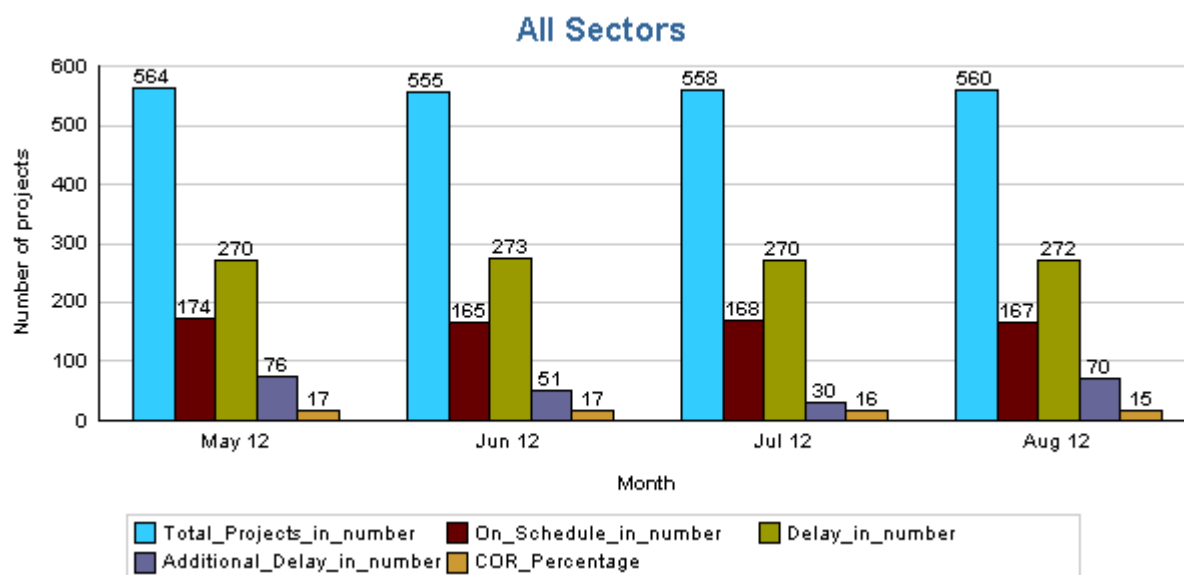


All Sectors Break-up of 272 Delayed projects in August 2012

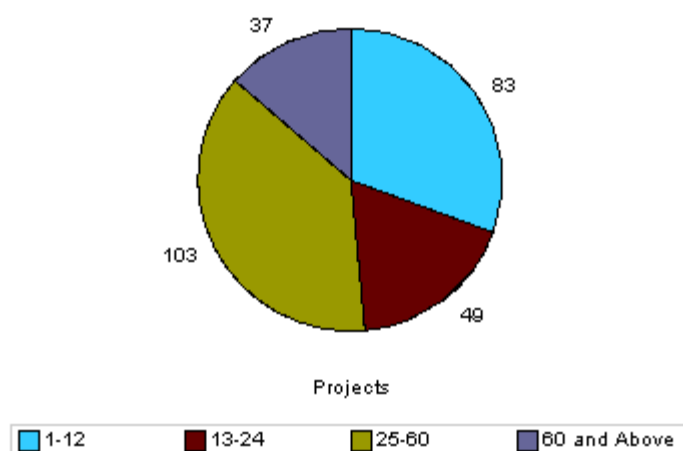


Trend and Graphical Analysis


Urban Development Sector

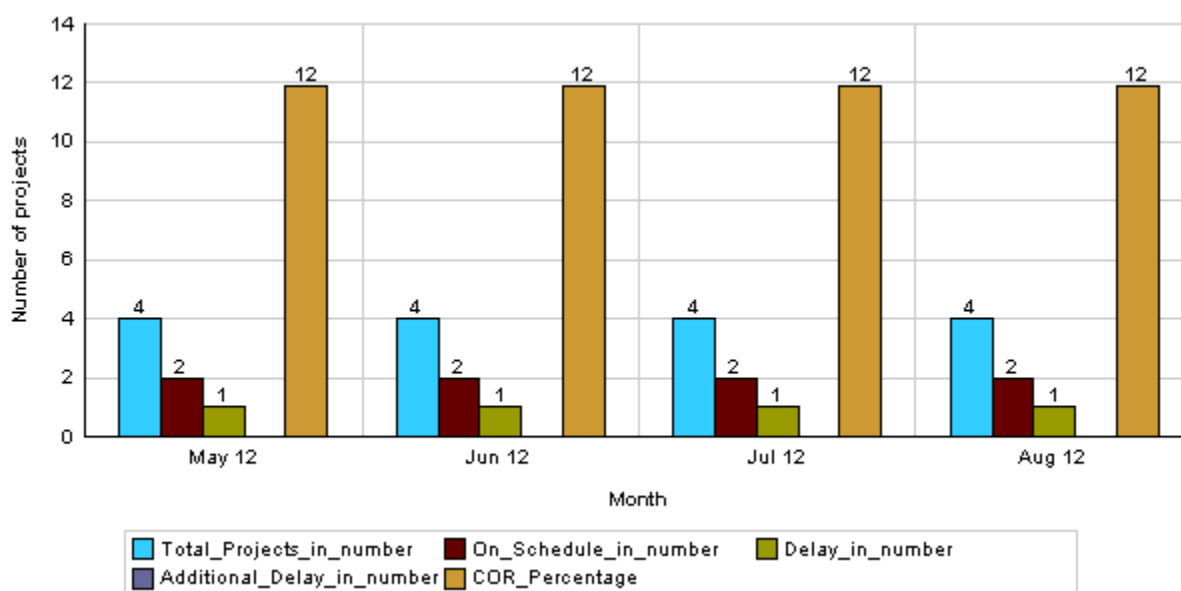


Urban Development Sector Sector Break-up of 1 Delayed projects in August 2012

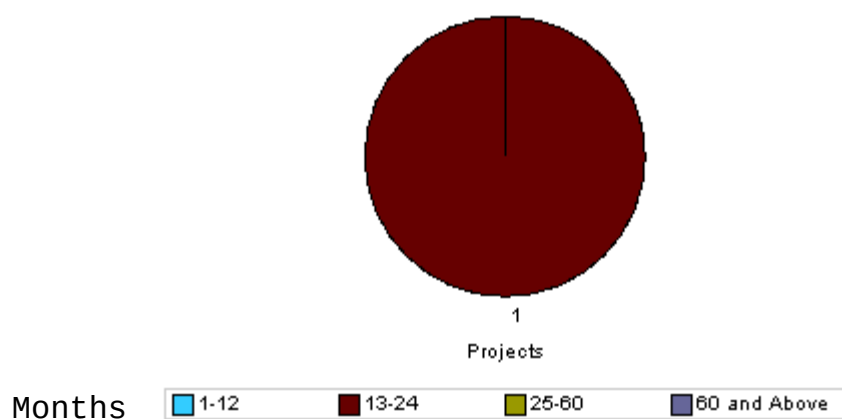


Trend and Graphical Analysis Telecommunications Sector

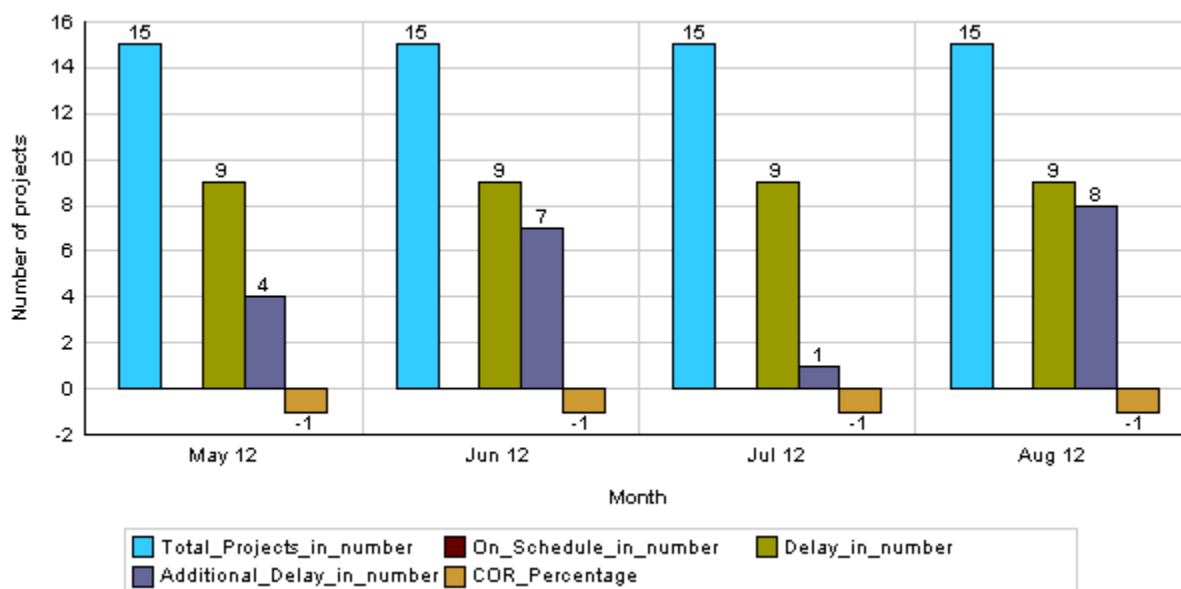


Telecommunications Sector Break-up of 9 Delayed projects in August 2012

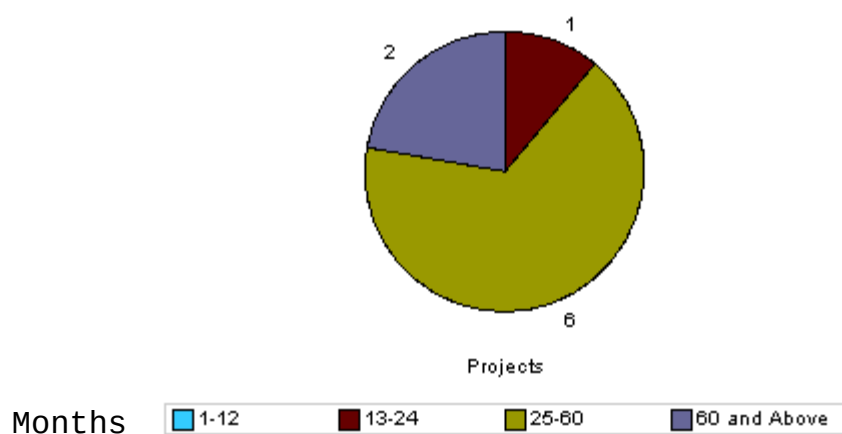


Trend and Graphical Analysis Shipping and Ports Sector

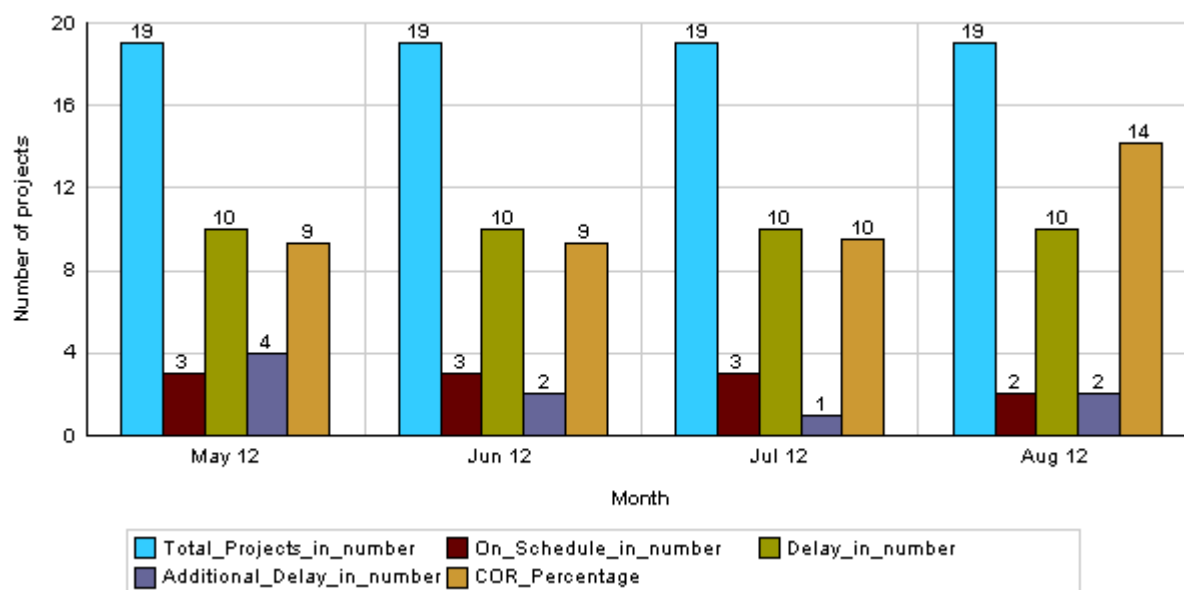


Sector Break-up of 10 Delayed projects in August 2012

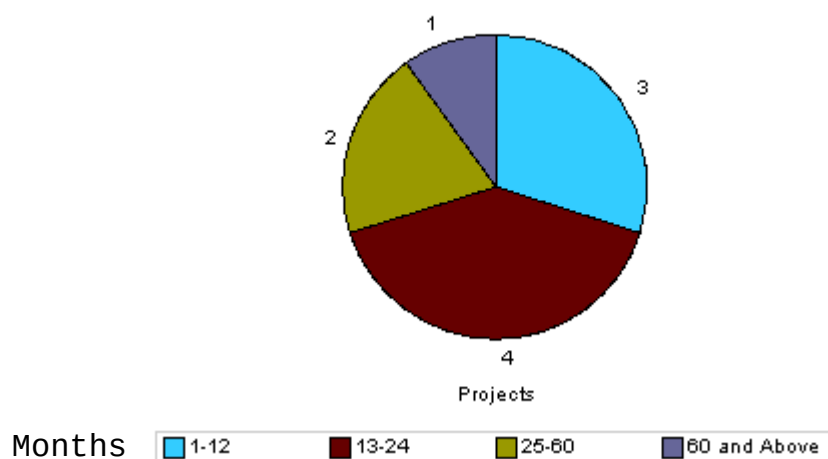

Trend and Graphical Analysis Road Transport and Highways Sector

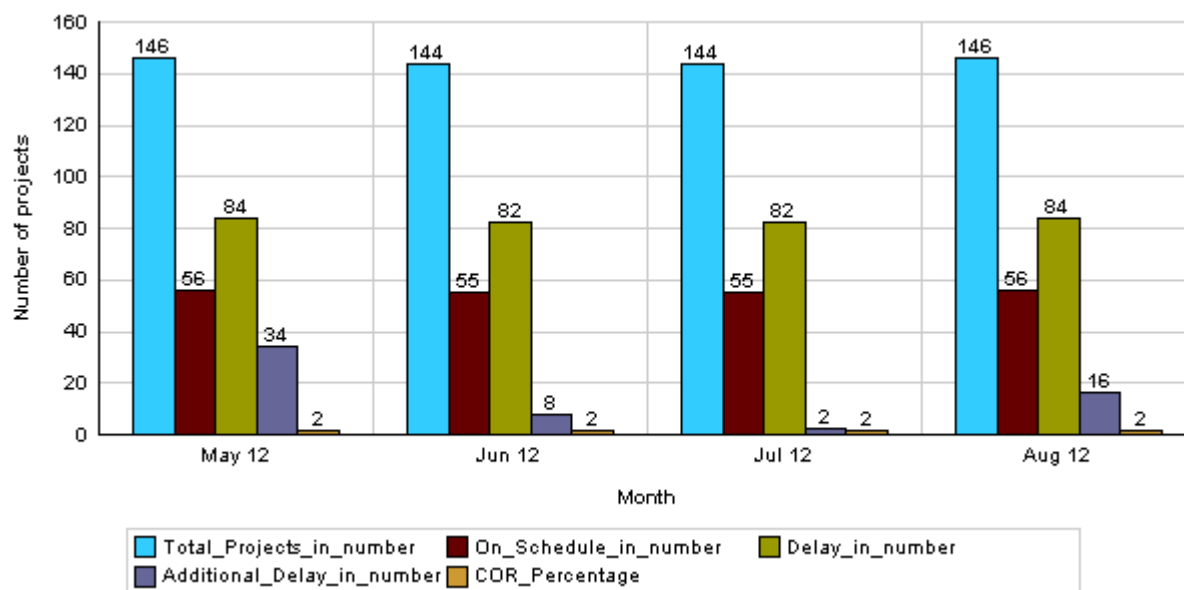


Sector Break-up of 84 Delayed projects in August 2012

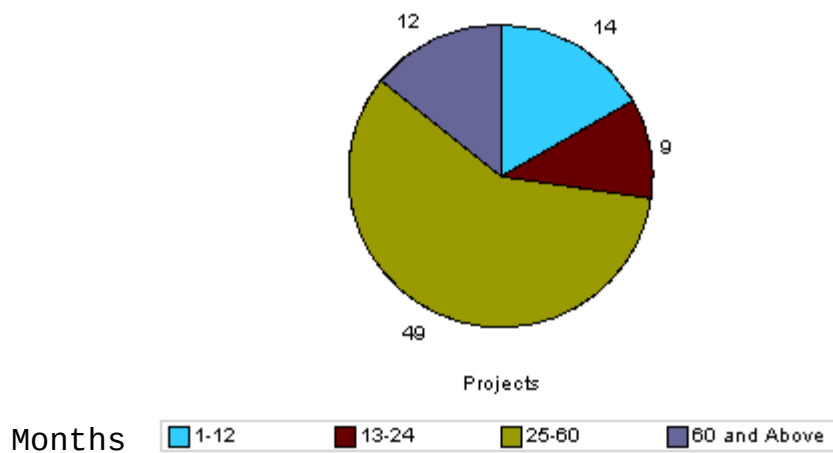


Trend and Graphical Analysis

Railways Sector

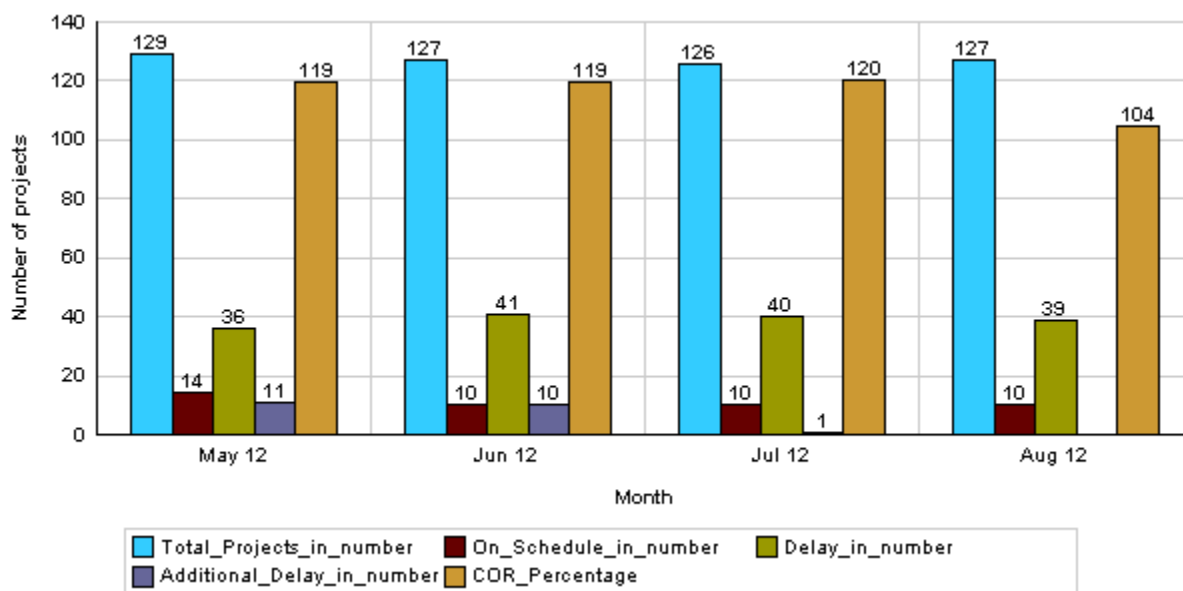


Railways Sector Break-up of 39 Delayed projects in August 2012

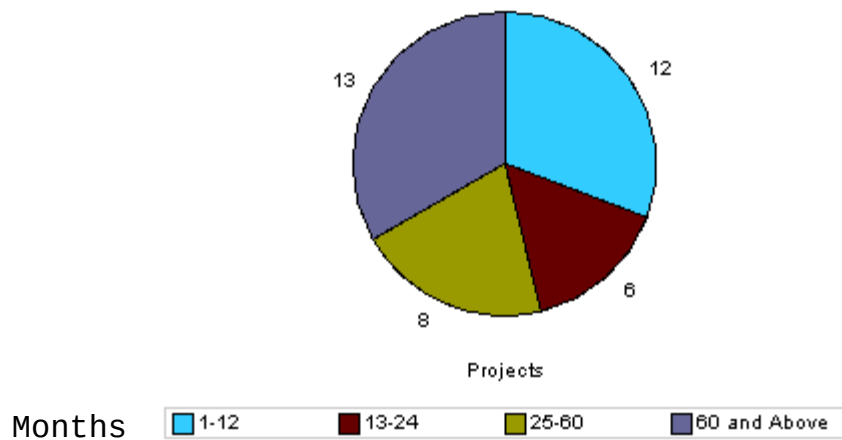


Trend and Graphical Analysis

Power Sector

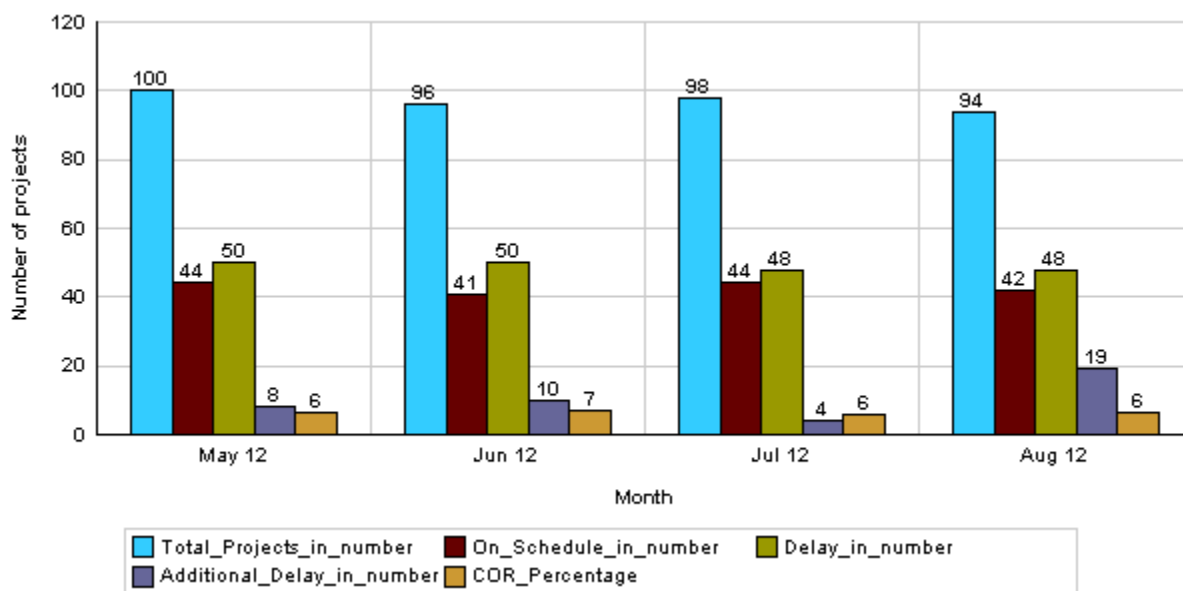


Power Sector Sector Break-up of 48 Delayed projects in August 2012

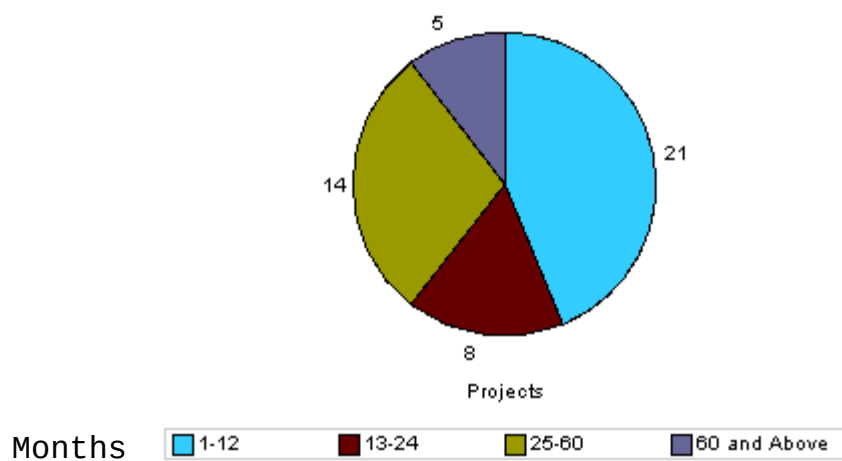


Trend and Graphical Analysis

Petroleum Sector

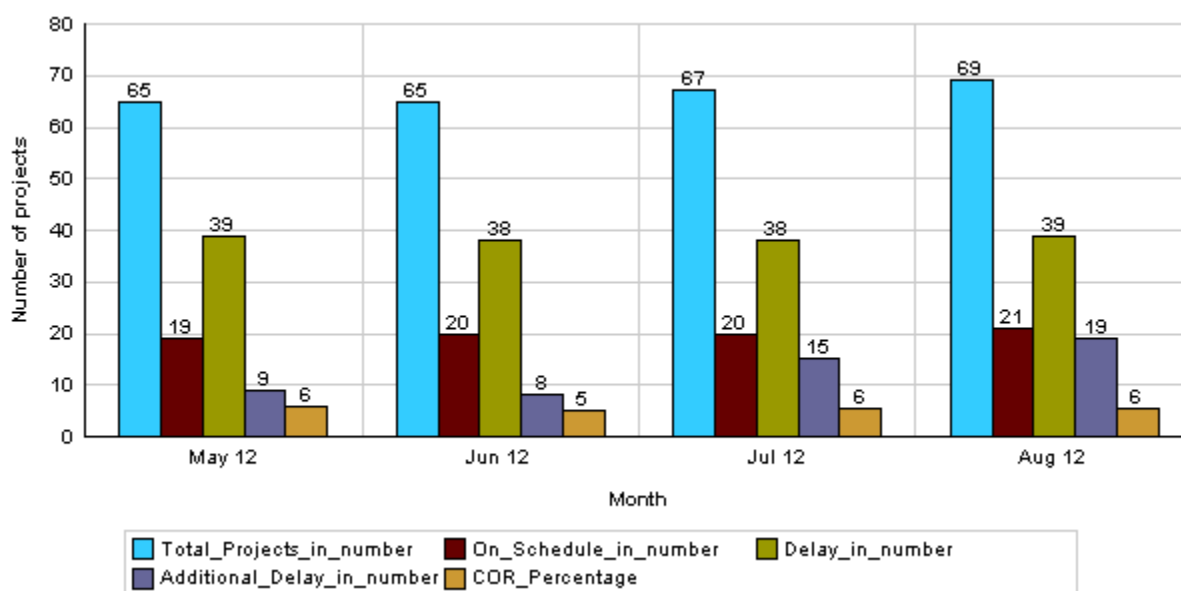


Petroleum Sector Sector Break-up of 39 Delayed projects in August 2012

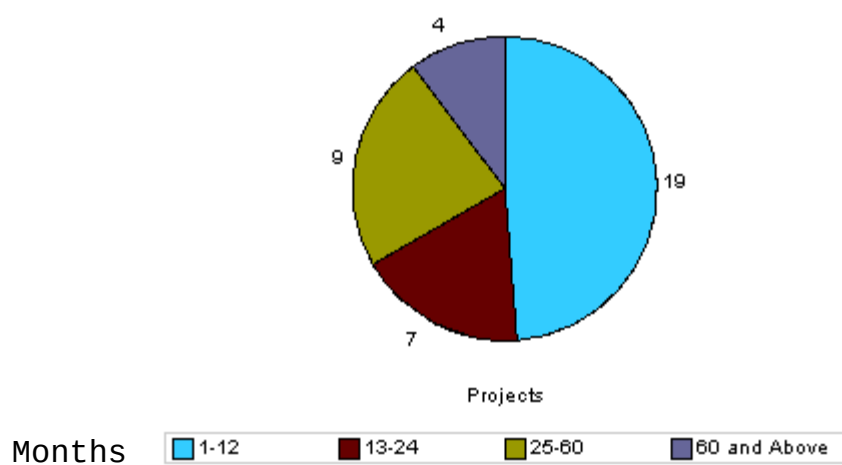


Trend and Graphical Analysis

Steel Sector

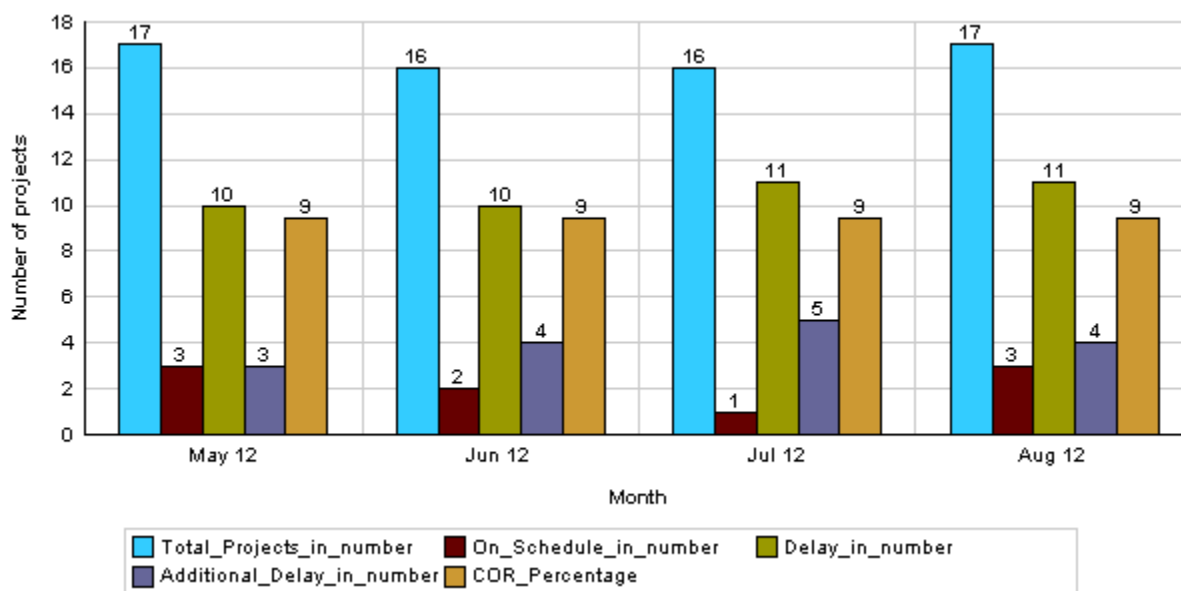


Steel Sector Sector Break-up of 11 Delayed projects in August 2012

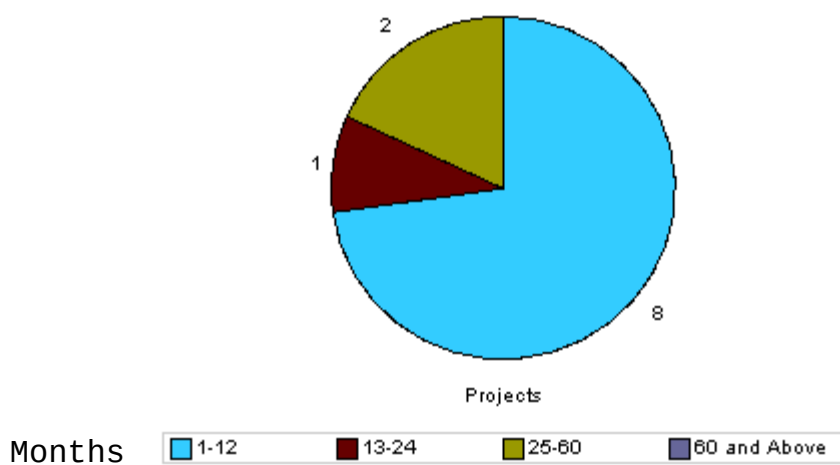


Trend and Graphical Analysis

Fertilisers Sector

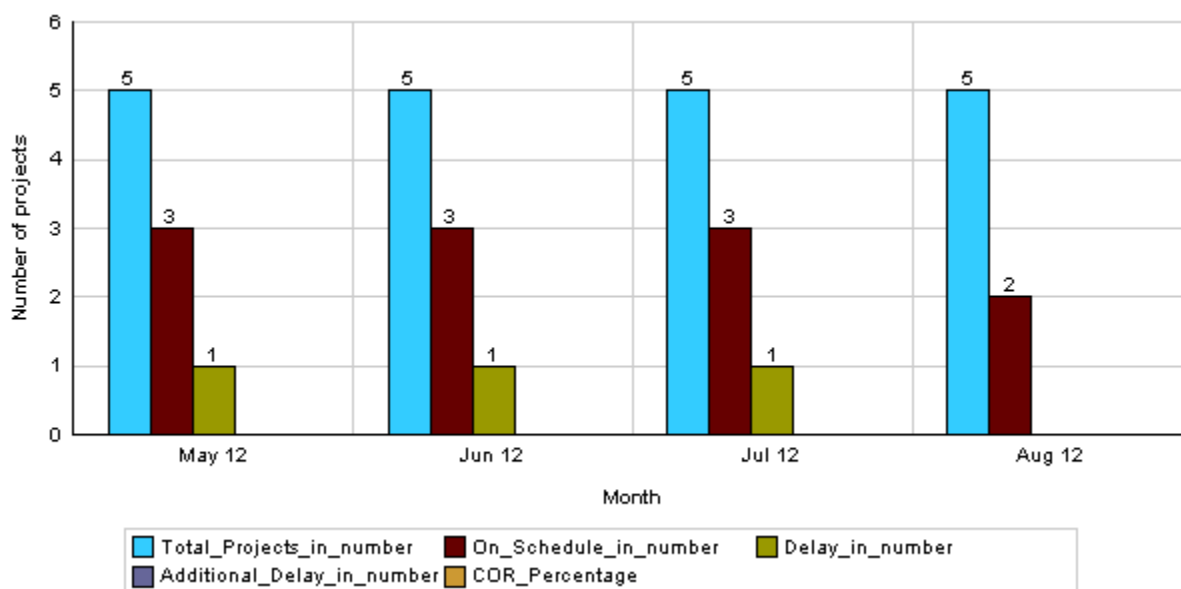


Fertilisers Sector Break-up of 0 Delayed projects in August 2012




Trend and Graphical Analysis

Coal Sector

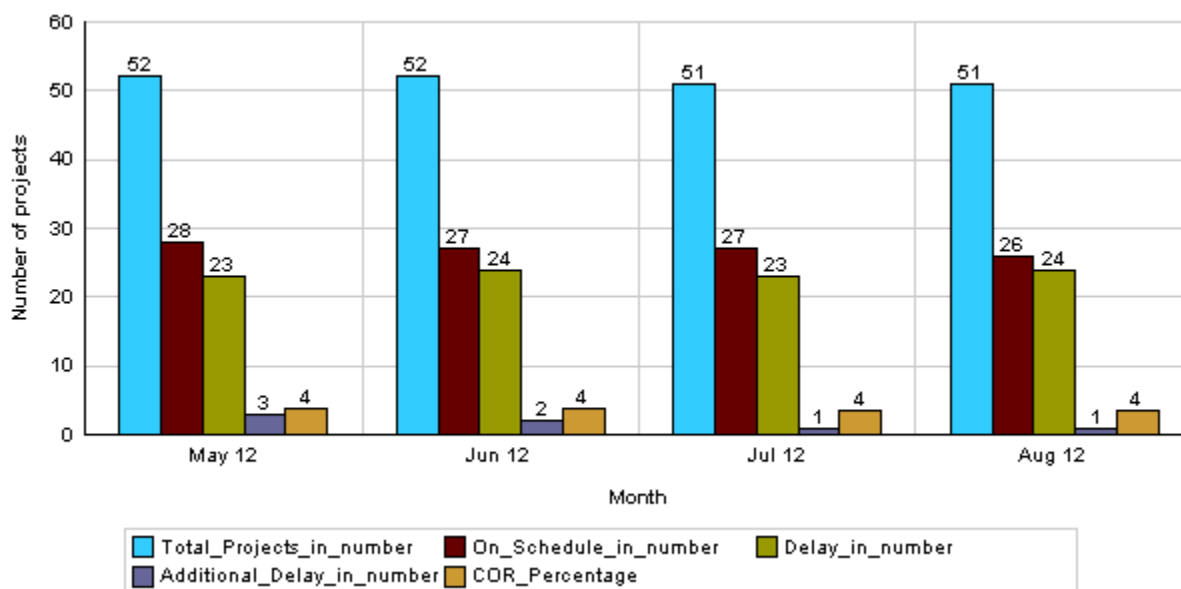


Coal Sector Sector Break-up of 24 Delayed projects in August 2012

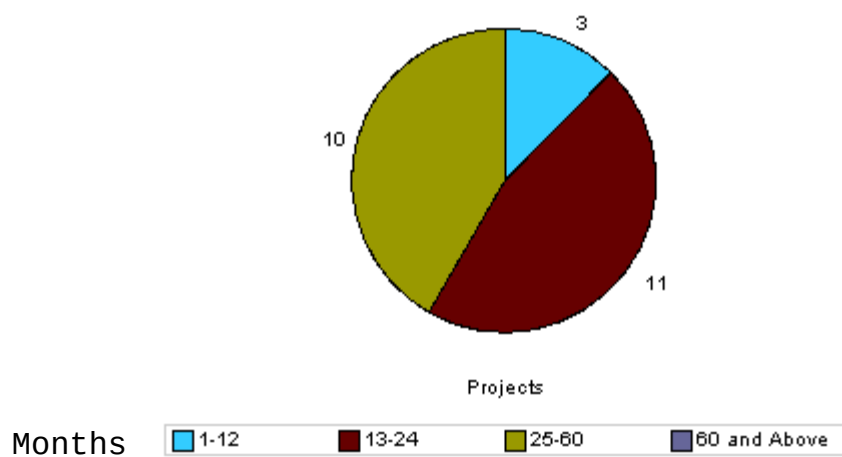


Trend and Graphical Analysis

Civil Aviation Sector

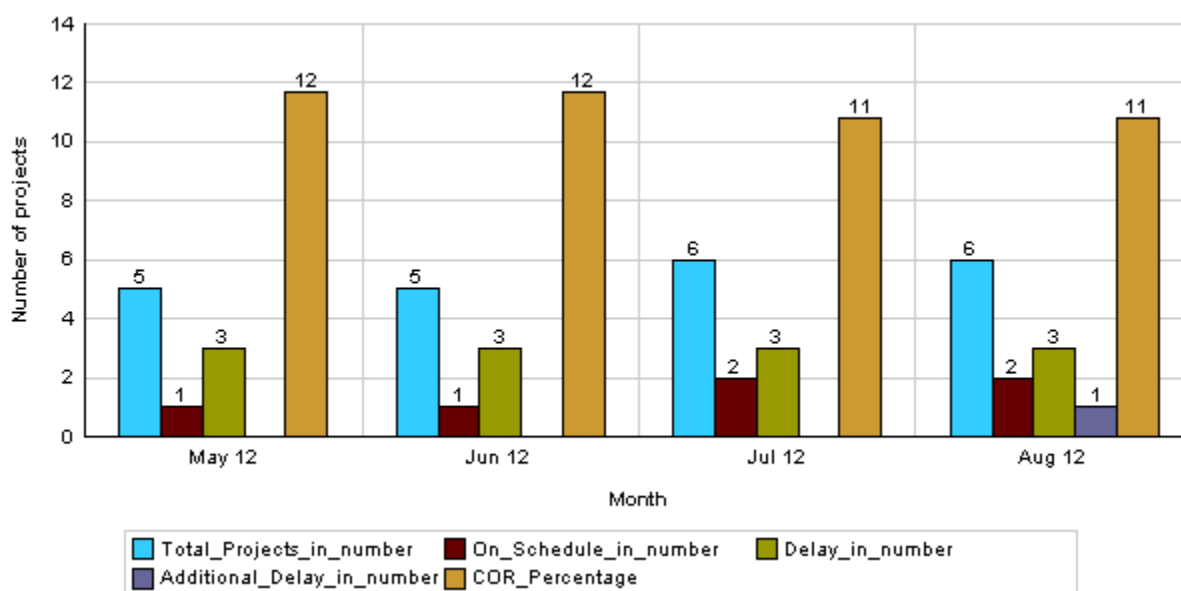


Civil Aviation Sector Sector Break-up of 3 Delayed projects in August 2012

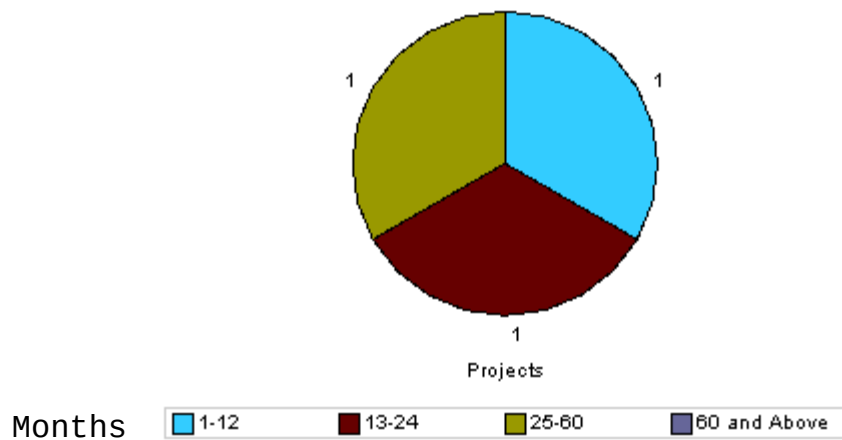


Trend and Graphical Analysis

Atomic Energy Sector

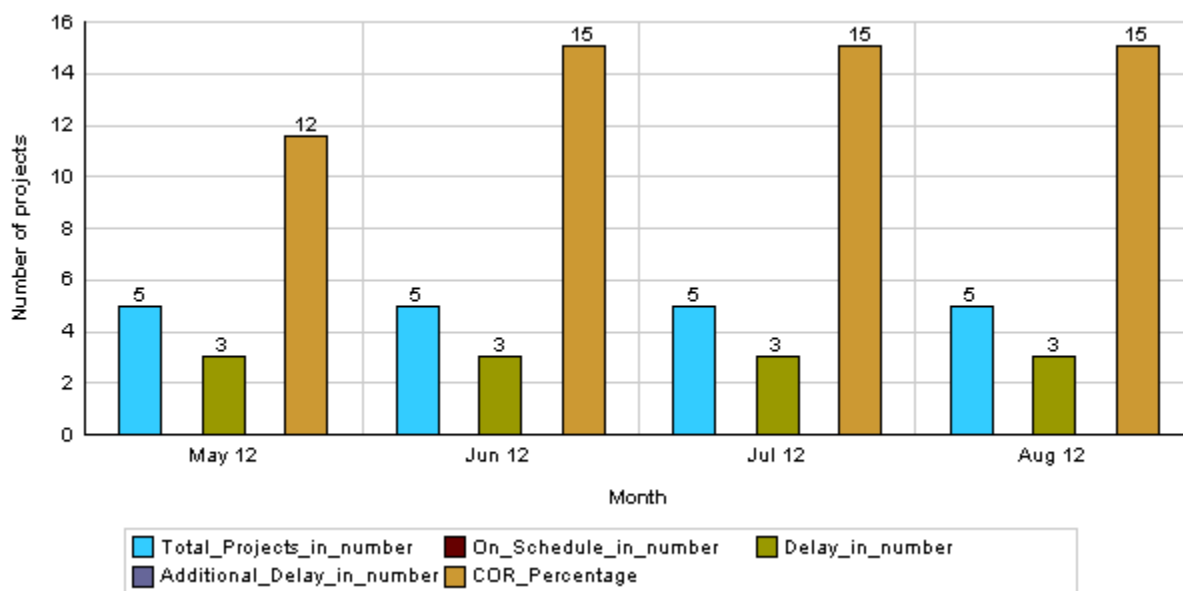

Atomic Energy Sector Break-up of 3 Delayed projects in August 2012

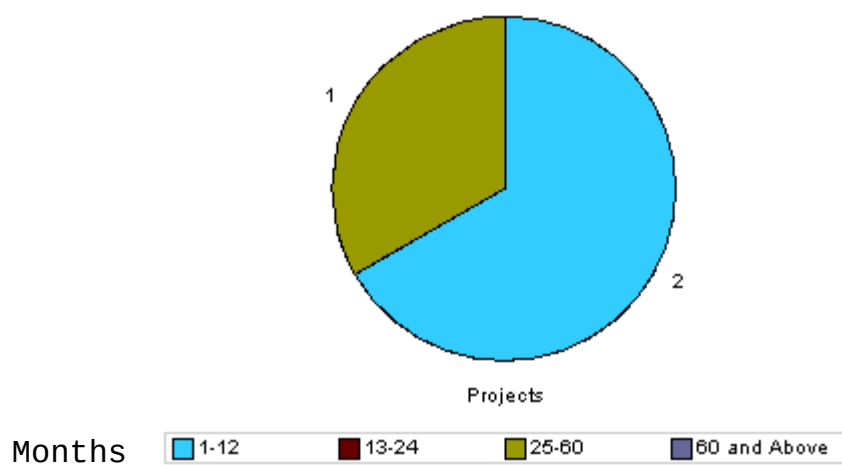

Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)			
		Original	Latest	Anticipated	Cumm Expenditure
Atomic Energy	5	41,548.29	41,548.29	47,832.29	22,654.84
Civil Aviation	6	5,473.58	5,680.58	6,063.07	4,446.95
Coal	51	36,056.46	37,022.46	37,312.25	12,653.88
Fertilisers	5	4,828.66	4,828.66	4,828.66	2,453.98
Steel	17	65,285.87	71,161.15	71,443.41	42,455.98
Petrochemicals	1	5,460.61	8,920.00	8,920.00	5,197.24
Petroleum	69	157,954.47	171,901.12	166,783.98	79,387.86
Power	94	224,936.05	228,743.15	238,936.53	101,520.58
Railways	127	64,518.68	93,061.58	131,959.43	62,072.84
Road Transport & Highways	146	92,448.72	92,615.22	94,027.34	66,341.65
Shipping & Ports	19	16,242.52	18,400.64	18,554.09	8,123.81
Telecommunications	15	6,161.00	6,164.88	6,101.79	1,786.40
Urban Development	4	44,245.18	44,304.08	49,518.08	3,047.06
Water Resources	1	542.90	542.90	1,187.00	35.49
Grand total	560	765,702.99	824,894.71	883,467.92	412,178.56

Sector Wise Details

(Aug,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>Atomic Energy</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00	11,459.00	1,826.00	12/2015	11/2016	11(O)	0/70
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00	17,270.00	14,945.00	12/2008	03/2013	51(O)	39/106
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00	5,677.00	3,641.60	09/2010	01/2012	-	6/80
4	RAJASTHAN ATOMIC POWER PROJECT - 7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00	12,320.00	1,158.00	12/2016	03/2017	3(O)	0/69
5	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29	1,106.29	1,084.24	04/2011 04/2011	04/2012	-	0/0
	Total		41,548.29	47,832.29	22,654.84				45/325
	<u>Civil Aviation</u>								
6	C/O INTEGRATED PASSENGER TER. BULD. NSCB AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51	2,325.00	2,081.48	05/2011 03/2012	10/2012	17(O) 7(R)	0/0
7	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46	309.46	185.18	01/2011 04/2013	04/2013	27(O) 0(R)	0/0
8	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61	335.61	130.41	05/2012	12/2012	7(O)	0/0
9	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	2,015.00	1,676.63	01/2011 02/2012	02/2012	-	0/0
10	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT - [N04000070]AAI,Punjab	02/2011	452.00	452.00	1.20	02/2015	02/2015	0(O)	0/0
11	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00	626.00	372.05	06/2013	06/2013	0(O)	0/0
	Total		5,473.58	6,063.07	4,446.95				0/0
	<u>Coal</u>								
12	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	09/2006	212.34 779.26	779.26	310.04	03/2013 09/2012	10/2014	19(O) 25(R)	7/22
13	AMLAI OC EXPANSION SECTOR 1.50 MTY - [N06000082]SECL,Chhatisgarh	11/2009	150.59	198.59	84.63	03/2016	03/2016	0(O)	2/6

Sector Wise Details

(Aug,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original /Revised (in months)	Milestone Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
14	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]NCL,Madhya pradesh	05/2006	1,352.04 1,143.54	1,143.54	357.39	03/2014 03/2016	03/2016	24(O) 0(R)	2/2
15	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Orissa	08/2008	207.28 -	207.28	100.35	03/2012 -	03/2014	24(O) -	5/7
16	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhandd	04/2006	471.66 341.63	341.63	108.37	03/2011 -	03/2013	24(O) -	0/2
17	BALRAM OCP EXTENSION,MCL (8.00 Mty) - [N06000044]MCL,Orissa	12/2007	172.08 -	172.08	117.83	03/2010 -	03/2015	60(O) -	4/4
18	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,Chhatisgarh	04/2012	258.56 -	258.56	39.30	03/2016 -	03/2016	0(O) -	0/0
19	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]MCL,Orissa	12/2007	490.00 -	490.10	115.68	03/2017 -	03/2017	0(O) -	6/12
20	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019]NCL,Multi State	11/2006	168.97 168.97	168.97	40.35	03/2014 03/2014	03/2014	0(O) 0(R)	1/2
21	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04 535.10	535.10	162.00	03/2012 03/2015	03/2015	36(O) 0(R)	0/0
22	Batura OCP (2.0 MTY) - [N06000049]SECL,Madhya pradesh	09/2008	203.82 -	203.82	-	03/2015 -	03/2015	0(O) -	1/1
23	CHURCHA ROUG (1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35 -	462.35	263.01	03/2014 -	03/2016	24(O) -	2/7
24	Churi Benti UG - [N06000083]CCL,Jharkhandd	06/2007	163.51 -	163.51	34.46	03/2011 -	03/2014	36(O) -	1/2
25	DIPKA EXPANSION OCP (SECL) (20-25 MTY) - [060100094]SECL,Chhatisgarh	12/2009	1,943.66 -	1,943.66	1,211.06	03/2014 -	03/2014	0(O) -	6/12
26	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,Chhatisgarh	06/2010	2,675.67 -	2,675.67	1,383.91	03/2014 -	03/2014	0(O) -	10/15
27	GOPAL PRASAD OCP - [N06000042]MCL,Orissa	02/2008	395.87 -	395.87	71.12	03/2015 -	03/2015	0(O) -	2/12
28	HINGULA OC-II EXP PH-III (15 MTY) - [N06000068]MCL,Orissa	11/2008	479.63 -	479.63	109.71	03/2013 -	03/2013	0(O) -	5/7
29	JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh	09/2008	152.43 -	152.43	-	03/2015 -	03/2017	24(O) -	1/6
30	JALAGAM VENGALA RAO OCP - [N06000094]SCCL,Andhra Pradesh	07/2011	447.06 -	447.06	-	03/2015 -	03/2015	0(O) -	4/31
31	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	09/2007	467.78 -	467.78	12.31	03/2013 -	03/2013	0(O) -	4/83
32	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18 -	287.17	0.82	03/2011 -	03/2015	48(O) -	0/1
33	KAKATIYA LAONGWALL - [N06000048]SCCL,Multi State	12/2008	453.63 -	453.63	72.70	12/2012 -	03/2015	27(O) -	8/44
34	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Orissa	12/2007	457.77 -	457.77	110.47	03/2013 -	03/2013	0(O) -	6/11
35	KARMA OCP - [N06000088]CCL,Jharkhandd	06/2009	162.46 -	162.46	30.89	03/2014 -	03/2014	0(O) -	0/0
36	KARTALI (EAST) OCP(2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24(O) -	1/6
37	KHADIA EXPANSION OPENCAST PROJECT 4 TO 10 MTPA,GMT - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28 1,131.28	1,131.28	1.51	03/2018 03/2018	03/2018	0(O) 0(R)	0/0

Sector Wise Details

(Aug,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestone Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
38	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Uttar Pradesh	05/2006	789.88 741.62	741.62	334.32	03/2010 -	03/2013	36(O) -	2/2
39	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Orissa	01/2005	302.96 -	302.96	105.43	03/2010 -	03/2014	48(O) -	9/11
40	KUSMUNDA EXPN.OCP(SECL)(10-15MTY) - [N06000008]SECL,Chhatisgarh	06/2008	1,188.31 -	1,188.31	668.76	03/2013 -	03/2013	0(O) -	0/8
41	Kistaram OCP - [N06000089]SCCL,Andhra Pradesh	11/2010	242.29 -	242.29	-	03/2015 -	03/2015	0(O) -	0/28
42	MAGADH OC (CCL) - [N06000015]CCL,Jharkhandd	07/2006	469.78 -	706.40	19.23	07/2012 -	03/2016	44(O) -	1/2
43	MANIKPUR OC EXPANSION - [N06000081]SECL,Chhatisgarh	11/2009	321.42 -	321.50	203.67	03/2014 -	03/2014	0(O) -	1/5
44	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19 -	181.19	39.22	03/2012 -	03/2013	12(O) -	10/34
45	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhandd	08/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015	0(O) -	0/0
46	Muraidih UG - [N06000096]BCCL,Jharkhandd	02/2011	339.88 -	339.88	-	04/2014 -	04/2014	0(O) -	0/0
47	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu	06/2011	5,907.11 -	5,907.11	22.16	12/2015 -	08/2017	20(O) -	0/33
48	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40 -	259.40	1.20	03/2012 -	03/2015	36(O) -	0/1
49	North Urimari OCP - [N06000084]CCL,Jharkhandd	12/2007	179.87 -	179.87	60.69	03/2012 -	03/2014	24(O) -	0/2
50	PELMA OCP(10.00MTY) - [N06000045]SECL,Chhatisgarh	07/2008	448.32 -	448.32	-	03/2015 -	03/2015	0(O) -	1/1
51	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77 -	339.77	0.83	03/2014 -	03/2016	24(O) -	0/1
52	Purnadih OCP - [N06000085]CCL,Jharkhandd	07/2008	210.98 -	210.98	87.89	03/2013 -	03/2013	0(O) -	0/2
53	RAJMAHAL OC EXP. - [N06000056]ECL,Multi State	09/2009	153.82 -	153.82	25.44	03/2014 -	03/2014	0(O) -	0/1
54	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97 -	418.97	95.86	03/2012 -	03/2013	12(O) -	24/27
55	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,Andhra Pradesh	07/2011	162.76 -	162.76	2.48	03/2015 -	03/2015	0(O) -	4/29
56	RKP OCP PHASE-I - [N06000079]SCCL,Andhra Pradesh	03/2010	209.78 -	209.78	26.63	03/2015 -	03/2015	0(O) -	4/31
57	Rajrappa RCE OCP - [N06000087]CCL,Jharkhandd	12/2009	510.85 -	510.85	268.59	03/2016 -	03/2016	0(O) -	1/2
58	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03 -	249.03	47.24	03/2012 -	-	- -	11/42
59	TALABIRA OCP - [N06000043]MCL,Orissa	03/2008	447.72 -	447.72	44.49	03/2016 -	03/2016	0(O) -	1/12
60	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 3,027.59	3,027.59	2,460.35	06/2009 -	03/2013	45(O) -	19/24
61	TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 -	4,909.54	3,296.75	03/2012 -	03/2014	24(O) -	0/39

Sector Wise Details

(Aug,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestone Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
62	Tapin OCP - [N06000086]CCL,Jharkhandd	08/2008	264.68	264.68	104.74	03/2012	03/2013	12(O)	0/2
			-	-	-	-	-	-	-
	Total		36,056.46	37,312.25	12,653.88				166/634
			-	-	-				
	<u>Fertilisers</u>								
63	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJ - [N08000005]NFL,Punjab	01/2010	1,294.19	1,294.19	639.95	01/2013	01/2013	0(O)	0/5
			-	-	-	-	-	-	-
64	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00	438.00	239.93	07/2011	07/2012	-	0/0
			-	-	-	-	-	-	-
65	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00	325.00	185.10	07/2011	04/2012	-	0/0
			-	-	-	-	-	-	-
66	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,Punjab	01/2010	1,478.63	1,478.63	718.00	01/2013	12/2012	-1(O)	8/8
			-	-	-	12/2012	-	0(R)	-
67	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJE - [N08000004]NFL,Haryana	01/2010	1,292.84	1,292.84	671.00	01/2013	01/2013	0(O)	0/5
			-	-	-	-	-	-	-
	Total		4,828.66	4,828.66	2,453.98				8/18
			-	-	-				
	<u>Steel</u>								
68	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,Karnataka	04/2011	572.00	572.00	165.84	-	04/2013	-	11/19
			-	-	-	-	-	-	-
69	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00	350.00	246.19	08/2010	10/2012	26(O)	0/1
			-	-	-	08/2010	-	26(R)	-
70	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00	343.58	248.53	02/2011	12/2012	22(O)	2/3
			-	-	-	02/2011	-	22(R)	-
71	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,Karnataka	02/2011	898.55	898.55	106.43	-	05/2013	-	10/21
			-	-	-	-	-	-	-
72	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00	450.00	205.20	05/2012	02/2013	9(O)	1/2
			-	-	-	05/2012	-	9(R)	-
73	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89	607.17	339.69	12/2011	10/2012	10(O)	16/21
			607.17	-	-	03/2012	-	7(R)	-
74	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	08/2007	108.00	216.68	91.83	10/2012	12/2012	2(O)	3/4
			-	-	-	10/2012	-	2(R)	-
75	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, Chattisga - [N12000078]SAIL,Delhi	07/2012	332.65	332.65	-	08/2014	08/2014	0(O)	0/0
			-	-	-	-	-	-	-
76	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON - [N12000075]SAIL,Orissa	11/2011	254.55	254.55	11.38	11/2013	03/2014	4(O)	0/1
			-	-	-	-	-	-	-
77	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	17,265.00	17,265.00	6,043.92	03/2013	09/2013	6(O)	19/27
			-	-	-	-	-	-	-
78	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhandd	01/2008	6,325.00	6,325.00	2,874.30	12/2011	12/2012	12(O)	10/16
			-	-	-	-	-	-	-

Sector Wise Details

(Aug,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
79	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL, West Bengal	06/2009	2,875.00	2,875.00	1,062.04	12/2012	03/2013	3(O)	7/12
80	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL, West Bengal	02/2008	14,443.00	16,408.00	13,628.33	12/2011	12/2012	12(O)	16/19
81	EXPANSION OF RINL/VSP FROM 3 MTPY- 6.3 MTPY OF LIQUID STEEL - [120100067]RINL, Andhra Pradesh	10/2005	8,692.00	12,291.00	9,726.00	10/2009	03/2013	41(O) 0(R)	60/64
82	Expansion of Rourkela Steel Plant - [N12000056]SAIL, Orissa	09/2008	11,812.00	11,812.00	7,706.30	11/2013	03/2013	-8(O)	6/14
83	INSTALLATION OF 1x45 MVA Submerged Arc Furnace AT - [N12000076]SAIL, Maharashtra	12/2011	187.33	187.33	-	12/2013	12/2013	0(O)	0/0
84	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Oddisha - [N12000079]SAIL, Delhi	01/2012	254.90	254.90	-	12/2014	12/2014	0(O)	0/0
	Total		65,285.87	71,443.41	42,455.98				161/224
	Petrochemicals								
85	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, Assam	04/2006	5,460.61	8,920.00	5,197.24	12/2013	12/2013	0(O)	13/29
	Total		5,460.61	8,920.00	5,197.24				13/29
	Petroleum								
86	102 MW WIND POWER PROJECT - [N16000119]ONGC, Rajasthan	07/2010	1,106.00	820.00	-	06/2012	10/2013	16(O)	0/0
87	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC, Multi State	01/2010	2,163.64	2,163.64	1,140.31	06/2012	06/2013	12(O)	0/0
88	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC, Gujarat	02/2008	370.11	370.11	249.90	04/2011	10/2012	18(O)	0/0
89	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC, Maharashtra	10/2008	1,797.35	977.00	479.00	12/2011	01/2013	13(O)	0/0
90	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, Assam	03/2009	2,465.15	2,378.86	938.59	03/2013	03/2014	12(O)	0/0
91	Ahmedabad Redevelopment - [N16000120]ONGC, Gujarat	11/2010	1,916.10	1,916.10	614.17	12/2014	12/2014	0(O)	0/0
92	Ankleswar Redevelopment - [N16000122]ONGC, Gujarat	11/2010	2,189.63	2,189.63	-	12/2014	12/2014	0(O)	0/0
93	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL, Multi State	12/2009	540.92	460.70	250.95	07/2012	06/2013	11(O) 11(R)	0/16
94	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]IOCL, Haryana	11/2009	341.50	341.50	110.19	02/2013	02/2013	0(O)	34/42
95	Butene-1 at Panipat - [N16000139]IOCL, Haryana	02/2012	190.00	190.00	4.54	03/2014	03/2014	0(O)	0/0
96	CDU/VDU-II - [N16000110]CPCL, Tamil Nadu	03/2010	333.99	333.99	177.15	-	09/2012	-	33/36
97	COMPRESSOR STATIONS (KAILARAS AND CHAINSA) - [N16000054]GAIL, Multi State	11/2007	1,167.00	798.00	732.04	04/2011	09/2012	17(O) 9(R)	2/2

Sector Wise Details

(Aug,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
98	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	287.21	09/2011 -	08/2013	23(O) -	0/0
99	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	5,557.03	05/2010 05/2012	10/2012	29(O) 5(R)	0/0
100	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 394.00	394.00	355.45	- 08/2011	-	-	0/22
101	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER - [N16000127]ONGC,Assam	06/2010	202.94 -	202.94	0.20	01/2014 -	01/2014	0(O) -	0/0
102	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79 -	756.65	11.81	05/2013 -	05/2013	0(O) -	0/0
103	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	269.10	-	08/2013 -	01/2014	5(O) -	0/0
104	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	240.95	43.73	09/2012 -	06/2013	9(O) -	0/0
105	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	723.64	-	03/2013 -	11/2013	8(O) -	0/0
106	Construction of tanks and blending facility at Vad - [N16000115]IOCL,Gujarat	02/2009	267.00 -	267.00	208.23	09/2012 09/2012	09/2012	0(O) 0(R)	0/0
107	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State	06/2009	4,543.43 4,508.38	2,300.00	1,869.00	03/2012 08/2012	12/2012	9(O) 4(R)	0/17
108	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip) - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	1,584.00	22.91	- -	-	-	0/0
109	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	06/2013	86(O) 12(R)	0/0
110	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	3,761.86	08/2010 03/2012	12/2013	40(O) 21(R)	0/0
111	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,858.42	09/2010 03/2012	04/2013	31(O) 13(R)	0/0
112	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	868.04	07/2010 05/2012	05/2013	34(O) 12(R)	0/0
113	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	04/2013	52(O) 0(R)	0/0
114	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 2,174.00	2,174.00	1,092.04	09/2012 09/2012	09/2012	0(O) 0(R)	0/76
115	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	1,282.33	09/2011 03/2012	09/2012	12(O) 6(R)	0/0
116	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	61.66	03/2013 -	04/2013	1(O) -	0/0
117	Development of C-26 Cluster Fields - [N16000133]ONGC,Maharashtra	03/2012	2,592.17 -	2,592.17	-	05/2014 -	05/2014	0(O) -	0/0
118	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 -	3,241.03	356.20	03/2013 -	04/2014	13(O) -	0/0

Sector Wise Details

(Aug,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
119	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44	410.44	43.99	11/2012	10/2013	11(O)	0/0
120	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00	2,523.00	176.69	01/2014	01/2014	0(O)	0/0
121	Development of Western Periphery of MH South Field - [N16000136]ONGC,Multi State	04/2012	600.17	600.17	-	12/2014	12/2014	0(O)	0/0
122	EURO-IV DHDT - [N16000109]CPCL,Tamil Nadu	09/2008	2,615.69	2,615.69	1,941.28	-	09/2012	-	114/116
123	Fire water network at Uran - [N16000141]ONGC,Maharashtra	05/2010	171.68	171.68	-	06/2013	06/2013	0(O)	0/0
124	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]OCL,Uttar Pradesh	07/2010	1,000.00	1,000.00	186.44	01/2013	06/2013	5(O)	17/18
125	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MU - [N16000081]BPCL,Maharashtra	04/2008	825.00 1,827.00	1,827.00	611.55	04/2013 04/2013	04/2013	0(O) 0(R)	0/167
126	Heera and South Heera Redevelopment Ph-II - [N16000132]ONGC,Maharashtra	03/2012	5,608.40	5,608.40	-	05/2015	05/2015	0(O)	0/0
127	INTEGRATED OFFSHORE CRUDE OIL HANDLING FACILITIES - [N16000090]OCL,Orissa	12/2009	1,492.33	1,492.33	1,164.57	06/2012 03/2013	03/2013	9(O) 0(R)	8/8
128	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,535.19	03/2007 03/2017	03/2017	120(O) 0(R)	6/6
129	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	629.66	03/2007 03/2014	03/2014	84(O) 0(R)	3/3
130	IOR of B-173A Field - [N16000140]ONGC,Multi State	01/2012	352.49	352.49	-	03/2014	03/2014	0(O)	0/0
131	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	269.29	03/2006 03/2013	03/2013	84(O) 0(R)	6/6
132	Integrated Development of B-127 fields - [N16000131]ONGC,Maharashtra	12/2011	2,059.63	2,059.63	-	03/2015	03/2015	0(O)	0/0
133	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18	7,596.18	2.20	01/2013	07/2015	30(O)	0/0
134	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07	281.07	3.48	10/2010	12/2014	50(O)	0/0
135	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE - [N16000070]GAIL,Multi State	07/2009	238.68 302.00	302.00	217.12	- 01/2012	10/2012	- 9(R)	0/1
136	KOCHI KOOTTANAD BANGLORE MANGLORE PIPELINE PH-II - [N16000129]GAIL,Multi State	06/2009	2,915.00	2,915.00	1,057.23	12/2012 12/2012	12/2013	12(O) 12(R)	0/21
137	KOCHI-KOOTANAD BANGALORE-MANGALORE PIPELINE PROJEC - [N16000071]GAIL,Multi State	06/2009	348.00	261.00	196.33	03/2012 08/2012	09/2012	6(O) 1(R)	2/4
138	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 12,160.26	12,160.26	8,984.37	01/2012	11/2012	10(O)	0/0
139	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39	6,855.93	4,060.65	09/2012	09/2013	12(O)	0/0
140	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	7,084.38	05/2010 03/2013	03/2013	34(O) 0(R)	0/0

Sector Wise Details

(Aug,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
141	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00	3,823.00	701.81	04/2015	04/2015	0(O)	0/0
142	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	755.76	677.99	03/2011 05/2011	03/2013	24(O) 22(R)	0/0
143	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02	740.02	479.11	03/2010 03/2012	05/2013	38(O) 14(R)	0/0
144	PARADIP REFINERY PROJECT - [N16000058]IOCL,Orissa	02/2009	29,777.00	30,426.00	17,280.00	- 09/2013	09/2013	- 0(R)	60/100
145	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,Multi State	08/2009	1,793.00	1,793.00	676.77	09/2012	09/2012	0(O)	0/11
146	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00	8,140.00	1,588.37	02/2014	02/2014	0(O)	0/0
147	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	08/2009	246.81	246.81	184.00	04/2012	-	-	0/0
148	Pipeline Replacement Project-3 - [N16000137]ONGC,Multi State	04/2012	2,547.26	1,417.00	-	05/2014	05/2014	0(O)	0/0
149	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78	1,803.78	613.33	07/2012	04/2013	9(O)	0/0
150	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00	898.00	893.30	- 03/2012	08/2012	- 5(R)	0/53
151	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra	05/2008	333.40 837.54	656.51	656.90	05/2010 04/2012	07/2012	-	0/0
152	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	288.04	154.37	08/2012	03/2013	7(O)	0/0
153	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32	330.47	218.92	03/2012	09/2012	6(O)	13/20
154	Wax Project - [N16000101]NRL,Assam	06/2010	576.60	576.60	60.70	12/2013 12/2013	12/2013	0(O) 0(R)	0/0
Total			157,954.47	166,783.98	79,387.86				298/745
Power									
155	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33	7,075.33	5,319.00	08/2012	03/2013	7(O)	0/11
156	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32	1,347.32	1,067.60	02/2012	11/2012	9(O)	0/7
157	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12	1,075.12	640.00	05/2012	12/2012	7(O)	0/11
158	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36	1,736.36	994.40	06/2012	10/2012	4(O)	0/4
159	BARH STPP STAGE -II - [N18000047]JNTPC,Bihar	02/2008	7,341.04	7,341.04	4,551.00	08/2013	06/2014	10(O)	5/19

Sector Wise Details

(Aug,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
160	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97	8,693.00	7,288.00	12/2009 12/2014	03/2016	75(O) 15(R)	26/47
161	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35	4,375.35	3,250.00	07/2011	11/2014	40(O)	4/28
162	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J and K	08/2006	621.26	913.00	751.21	02/2011 10/2012	10/2012	20(O) 0(R)	2/4
163	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNA - [N18000111]PGCIL,Andhra Pradesh	08/2011	1,637.34	1,637.34	239.60	08/2014	08/2014	0(O)	0/20
164	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA - [N18000126]PGCIL,Andhra Pradesh	03/2012	206.44	206.44	22.20	06/2014	06/2014	0(O)	0/20
165	Common System Associated with Coastal Energen Priv - [N18000103]PGCIL,Tamil Nadu	09/2011	1,940.13	1,940.13	243.10	09/2014	09/2014	0(O)	0/20
166	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96	975.96	867.25	10/2009	03/2013	41(O)	20/20
167	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80	1,272.80	384.60	11/2012	03/2014	16(O)	3/11
168	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123]PGCIL,Multi State	03/2012	198.63	198.63	-	09/2014	09/2014	0(O)	0/0
169	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA - [N18000101]PGCIL,Chhatisgarh	05/2011	1,961.87	1,961.87	368.10	05/2014	05/2014	0(O)	0/16
170	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52	1,719.52	582.60	08/2013	08/2013	0(O)	0/14
171	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,Bihar	12/2011	901.77	901.77	59.60	08/2014	08/2014	0(O)	0/21
172	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000107]PGCIL,Chhatisgarh	08/2011	1,391.97	1,391.97	343.00	12/2013	12/2013	0(O)	0/13
173	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32	160.32	48.80	10/2012	03/2013	5(O)	0/15
174	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45 1,007.16	1,007.16	842.33	12/2007 12/2009	-	-	0/10
175	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pr.	12/2004	2,496.90	2,496.90	1,954.52	05/2013 06/2016	03/2017	46(O) 9(R)	4/22
176	KISHANGANGA HEP - [N18000031]NHPC,J and K	07/2007	2,238.67 3,642.04	3,642.00	1,630.50	01/2016 01/2016	11/2016	10(O) 10(R)	0/2
177	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pr.	10/2002	4,527.15	4,527.15	4,448.00	04/2009 03/2014	03/2014	59(O) 0(R)	0/9
178	KUDGI STPP STAGE 1 - [N18000131]NTPC,Karnataka	12/2011	15,166.19	15,166.19	959.00	12/2016	12/2016	0(O)	0/0
179	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29 2,159.07	2,159.07	1,833.11	09/2008	12/2012	51(O)	17/37
180	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28	6,010.89	4,349.00	08/2012	03/2013	7(O)	10/16

Sector Wise Details

(Aug,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
181	MOUDA STPP STAGE 2 - [N18000132]NTPC,Maharashtra	03/2012	7,921.47	7,921.47	536.00	09/2016	09/2016	0(O)	0/0
182	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J and K	08/2006	611.01	936.00	786.38	08/2010 01/2013	01/2013	29(O) 0(R)	0/3
183	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19	11,130.19	4,951.10	08/2013	09/2014	13(O)	0/17
184	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29	410.29	241.00	02/2012	12/2013	22(O)	0/14
185	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48	520.48	316.20	11/2011	12/2013	25(O)	0/11
186	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66	509.66	335.80	11/2011	12/2013	25(O)	0/14
187	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68	182.68	47.10	01/2013	01/2013	0(O)	0/7
188	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64	752.64	196.30	07/2013	07/2013	0(O)	0/12
189	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57	1,677.57	512.00	04/2013	10/2013	6(O)	0/12
190	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII - [N18000091]PGCIL,Multi State	12/2010	209.78	209.78	70.90	08/2013	08/2013	0(O)	0/16
191	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,Multi State	11/2011	723.63	723.63	43.20	11/2014	11/2014	0(O)	0/0
192	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58	965.58	437.00	11/2012	03/2013	4(O)	0/10
193	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.56	2,716.00	1,893.71	10/2010 01/2013	06/2013	32(O) 5(R)	0/0
194	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pr.	09/2002	3,919.59	5,366.00	3,532.32	09/2009 07/2014	12/2017	99(O) 41(R)	1/20
195	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pr.	12/2008	573.99	573.99	383.57	08/2012 08/2013	09/2014	25(O) 13(R)	14/19
196	RAMPUR HEP(412 MW) - [N18000024]SJVN,L Himachal Pr.	01/2007	2,047.03	2,047.03	1,914.62	01/2012	09/2013	20(O)	0/0
197	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81	6,230.81	3,475.00	10/2012	05/2013	7(O)	10/16
198	SOLAPUR STTP - [N18000133]NTPC,Maharashtra	03/2012	9,395.18	9,395.18	666.00	11/2016	11/2016	0(O)	0/0
199	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pr.	09/2003	6,285.33	10,667.00	5,733.74	09/2010 08/2014	03/2017	78(O) 31(R)	11/11
200	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36	170.36	45.60	04/2013	04/2013	0(O)	0/15

Sector Wise Details

(Aug,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
201	SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95	2,360.95	1,948.00	08/2012	03/2013	7(O)	0/7
202	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BA - [N18000124]PGCIL,Madhya pradesh	03/2012	213.78	213.78	-	03/2014	03/2014	0(O)	0/0
203	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR - [N18000116]PGCIL,Chhatisgarh	12/2011	1,746.65	1,746.65	47.90	08/2014	08/2014	0(O)	0/20
204	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP P - [N18000120]PGCIL,Maharashtra	02/2012	1,310.85	1,310.85	102.50	02/2015	02/2015	0(O)	0/0
205	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,Multi State	06/2012	1,263.26	1,263.26	20.60	11/2014	11/2014	0(O)	0/0
206	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJEC - [N18000117]PGCIL,Chhatisgarh	01/2012	1,422.85	1,422.85	104.70	01/2015	01/2015	0(O)	0/19
207	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,Multi State	12/2011	297.33	297.33	22.20	08/2014	08/2014	0(O)	0/20
208	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,Multi State	10/2011	487.49	487.49	60.40	06/2014	06/2014	0(O)	0/19
209	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61	276.61	158.30	04/2012	10/2012	6(O)	0/0
210	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34	232.34	112.28	06/2012	10/2012	4(O)	0/9
211	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83	1,216.83	739.30	08/2012	12/2012	4(O)	0/11
212	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttaranchal	11/2006	2,978.48	2,978.48	1,528.00	-	09/2015	-	2/14
213	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38	1,501.75	1,173.29	09/2009 06/2013	08/2013	47(O) 2(R)	0/0
214	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92	1,628.00	1,551.34	03/2007 09/2012	01/2013	70(O) 4(R)	25/25
215	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00 2,978.86	2,978.86	371.17	07/2010 02/2016	02/2016	67(O) 0(R)	1/10
216	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000118]PGCIL,Gujarat	01/2012	259.28	259.28	14.60	01/2014	01/2014	0(O)	0/17
217	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARK - [N18000113]PGCIL,Multi State	12/2011	2,422.66	2,422.66	73.00	08/2014	08/2014	0(O)	0/0
218	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART - - [N18000129]PGCIL,Multi State	02/2012	3,201.44	3,201.44	45.80	10/2014	10/2014	0(O)	0/21
219	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37 386.32	386.32	328.83	07/2011	11/2012	16(O)	0/5

Sector Wise Details

(Aug,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
220	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12	4,824.12	2,896.40	10/2012	09/2013	11(O)	0/12
221	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR - [N18000077]PGCIL,West Bengal	04/2010	4,404.57	4,404.57	334.70	01/2015	01/2015	0(O)	0/20
222	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL,Multi State	03/2011	2,569.25	2,569.25	582.60	03/2014	03/2014	0(O)	0/15
223	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM - [N18000090]PGCIL,Andhra Pradesh	12/2010	779.21	779.21	525.10	08/2013	08/2013	0(O)	0/14
224	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000121]PGCIL,Andhra Pradesh	02/2012	324.33	324.33	1.90	08/2014	08/2014	0(O)	0/20
225	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000122]PGCIL,Andhra Pradesh	02/2012	1,927.16	1,927.16	33.90	10/2014	10/2014	0(O)	0/20
226	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24	758.75	589.00	01/2010	02/2013	37(O)	0/22
227	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19	184.19	151.20	11/2011	03/2013	16(O)	0/7
228	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88	7,031.88	3,810.70	12/2012	12/2012	0(O)	0/11
229	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT - [N18000114]PGCIL,Gujarat	12/2011	552.44	552.44	47.40	02/2014	02/2014	0(O)	0/20
230	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,Madhya pradesh	08/2011	425.51	425.51	90.10	10/2013	10/2013	0(O)	0/18
231	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93	181.93	48.40	07/2013	07/2013	0(O)	0/0
232	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CH - [N18000105]PGCIL,Multi State	09/2011	1,366.34	1,366.34	204.80	12/2013	12/2013	0(O)	0/18
233	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECT - [N18000104]PGCIL,Jharkhand	10/2011	558.26	558.26	63.80	11/2013	11/2013	0(O)	0/20
234	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Orissa	09/2010	2,074.86	2,074.86	647.30	03/2013	03/2013	0(O)	0/14
235	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Orissa	12/2010	2,743.19	2,743.19	775.80	12/2013	12/2013	0(O)	0/13
236	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99	4,672.99	1,505.60	11/2012	06/2013	7(O)	0/15

Sector Wise Details

(Aug,2012)

						Date of Commissioning		Delay w.r.t. Original /Revised (in months)	Milestone s Achieved/ Total	
S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	
237	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR - [N18000112]PGCIL,Chhatisgarh	11/2011	2,127.51 -	2,127.51	230.30	07/2014 -	07/2014	0(O) -	0/19	
238	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 623.44	623.44	325.05	- 07/2013	07/2013	- 0(R)	6/29	
239	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,Mizoram	01/2011	913.63 913.63	913.63	344.41	07/2014 02/2015	02/2015	7(O) 0(R)	0/16	
240	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	886.40	12/2012 -	03/2013	3(O) -	0/11	
241	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL,Multi State	03/2011	1,585.12 -	1,585.12	366.80	11/2013 -	11/2013	0(O) -	0/15	
242	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03 -	250.03	56.90	01/2013 -	11/2013	10(O) -	0/16	
243	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J and K	08/2005	1,729.29 -	2,083.00	1,772.30	11/2009 02/2013	03/2013	40(O) 1(R)	0/4	
244	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00 -	5,915.00	3,767.00	10/2012 -	03/2013	5(O) -	9/15	
245	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttaranchal	08/2008	2,491.58 2,491.58	3,422.44	316.25	07/2014 -	05/2016	22(O) -	1/3	
246	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23 -	5,221.23	3,153.00	07/2010 -	12/2012	29(O) -	20/20	
247	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	477.69	409.50	09/2010 -	-	-	0/9	
248	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,Chhatisgarh	03/2012	9,569.76 -	9,569.76	27.70	06/2015 -	06/2015	0(O) -	0/24	
Total			224,936.05 -	238,936.53	101,520.58					191/1231
Railways										
249	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 813.34	1,141.75	407.49	03/2014 -	03/2014	0(O) -	0/0	
250	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	227.42	250.82	12/2009 03/2011	03/2011	-	0/0	
251	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 1,010.00	2,200.00	182.53	- -	03/2013	- -	0/0	
252	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	453.04	392.26	03/2011 03/2011	03/2011	-	0/0	
253	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 405.17	548.95	518.45	06/1999 03/2011	03/2011	-	0/0	
254	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	1,214.00	96.96	- -	-	-	0/0	
255	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.14 404.39	404.39	0.49	03/2013 -	03/2013	0(O) -	0/0	
256	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 901.62	901.62	0.29	- -	-	-	0/0	

Sector Wise Details

(Aug,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
257	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, West Bengal	03/1998	111.90 1,028.05	1,412.74	448.10	03/2005 12/2008	06/2016	135(O) 90(R)	0/0
258	BARDHAMAN-KATWA (GC) - [N22000091]ER, West Bengal	04/2007	245.15 1,106.62	1,106.62	207.07	12/2010 03/2011	03/2011	-	0/0
259	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP, Maharashtra	03/1996	401.81 401.81	495.44	191.30	03/2004 12/2010	03/2014	120(O) 39(R)	0/0
260	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR, Mizoram	04/2008	619.34 619.34	2,393.48	11.78	04/2014 -	03/2015	11(O) -	0/0
261	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, Madhya Pradesh	09/2007	687.20 -	687.20	656.89	03/2010 -	12/2012	33(O) -	0/0
262	BILASPUR-URKURA (DL) - [220100321]RVNL, Chhattisgarh	04/1997	151.52 -	350.00	321.48	- 03/2009	03/2011	-	0/0
263	BPUTRA BRIDGE AT BOGIBIL & LINK LINES, NEFR - [220100201]NEFR, Assam	09/1997	1,000.00 1,500.00	3,230.01	2,408.10	04/2008 03/2014	12/2015	92(O) 21(R)	0/0
264	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER, West Bengal	04/1999	207.52 207.52	207.52	137.67	12/2012 -	05/2013	5(O) -	0/0
265	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR, Gujarat	04/2006	117.36 196.95	196.95	181.64	03/2011 -	03/2011	-	0/0
266	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR, Gujarat	04/2008	318.24 -	468.62	1.00	03/2012 -	03/2012	-	0/0
267	CALICUT-MANGALORE (DL) (SR) - [220100151]SR, Multi State	02/1996	240.00 -	579.37	600.41	- -	02/2012	-	0/0
268	CHANDIGARH-LUDHIANA(NEW BG LINE), NR - [220100241](NR), Punjab	07/1998	248.44 576.27	1,115.21	877.21	12/2012 01/2013	01/2013	1(O) 0(R)	0/0
269	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU, Bihar	03/2005	470.09 1,417.97	1,417.97	1,011.09	- -	03/2012	-	0/0
270	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, Madhya Pradesh	04/2005	383.79 -	585.93	194.91	- -	12/2013	-	0/0
271	CHURCHGATE-VIRAR: CONV. OF 1500V DC TRACTION TO 25 KV AC, WR - [220100233]RE, Maharashtra	07/1996	653.84 1,302.12	1,302.12	608.97	06/2013 06/2012	06/2012	-	0/0
272	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR, Arunachal Pr.	09/1996	156.00 -	415.73	240.93	- -	03/2012	-	0/0
273	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD) - [220100149]RVNL, Chhattisgarh	04/1995	304.00 -	968.60	110.02	12/2012 -	-	-	0/0
274	DANIWAN-BIHARSARIF (NL), ECR - [220100311]ECR, Bihar	04/2001	104.79 -	406.92	78.91	- -	-	-	0/0
275	DAUSA-GANGAPUR CITY(NL), NWR - [220100184]NWR, Rajasthan	02/1997	151.84 410.08	410.08	194.48	- -	03/2013	-	0/0
276	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER, Multi State	04/2000	138.00 607.09	607.09	407.33	12/2012 12/2012	02/2013	2(O) 2(R)	0/0
277	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR, Tamil Nadu	09/2006	343.17 343.17	900.00	542.57	- -	12/2012	-	0/0
278	Dakshin-barasal-lakshmikantapur - [N22000116]ER, West Bengal	04/2009	259.51 533.38	533.38	85.44	12/2011 02/2012	02/2012	-	0/0

Sector Wise Details

(Aug,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
279	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	171.10	141.55	03/2012 -	03/2012	-	0/0
280	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	250.00	227.48	03/2011 -	03/2012	-	0/0
281	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	495.74	162.22	06/2013 06/2013	03/2014	9(O) 9(R)	0/0
282	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	634.13	555.27	03/1995 -	03/2013	216(O) -	0/0
283	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	270.00	260.85	02/2011 02/2011	02/2013	24(O) 24(R)	0/0
284	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 261.70	261.70	56.12	02/2006 -	12/2013	94(O) -	0/0
285	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 381.17	863.23	580.64	- -	03/2012	-	0/0
286	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	1,038.00	590.26	03/1998 -	-	-	0/0
287	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	776.00	324.70	- 05/2009	05/2009	-	0/0
288	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	611.03	105.94	12/2011 11/2013	11/2013	23(O) 0(R)	0/0
289	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	324.66	180.42	- -	03/2015	-	0/0
290	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 1,185.00	1,185.00	219.71	- 09/2009	12/2011	-	0/0
291	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	337.30	222.07	- -	03/2012	-	0/0
292	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	944.55	509.89	- -	01/2013	-	0/0
293	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	230.03	145.43	- -	03/2014	-	0/0
294	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	499.16	168.27	03/2007 03/2007	03/2015	96(O) 96(R)	0/0
295	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00 -	997.58	69.57	- -	-	-	0/0
296	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 829.74	829.74	6.07	03/2015 -	03/2015	0(O) -	0/0
297	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30	847.76	833.20	06/2007 -	06/2007	-	0/0
298	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	1,043.55	659.06	03/2012 08/2012	02/2013	11(O) 6(R)	0/0
299	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	500.00	414.03	03/2012 03/2012	12/2012	9(O) 9(R)	0/0
300	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	4,444.00	911.23	03/2011 03/2014	03/2016	60(O) 24(R)	0/0

Sector Wise Details

(Aug,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
301	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 653.19	653.46	175.60	03/2014 -	03/2014	0(O) -	0/0
302	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 333.50	333.50	210.82	03/2012 03/2012	10/2012	7(O) 7(R)	0/0
303	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	1,577.46	1,354.57	- -	03/2012	-	0/0
304	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 323.40	750.89	495.55	- -	03/2014	- -	1/1
305	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 229.88	712.00	736.89	- -	10/2012	- -	0/0
306	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,041.79	730.92	12/2010 12/2010	03/2015	51(O) 51(R)	0/0
307	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	162.87	92.71	- -	03/2013	- -	0/0
308	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	225.00	212.13	03/2009 03/2009	04/2013	49(O) 49(R)	0/0
309	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	1,100.00	254.10	- -	03/2013	- -	0/0
310	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	359.86	1.22	- -	03/2015	- -	0/0
311	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd	04/1996	371.36 768.87	768.87	415.19	- 03/2010	03/2010	-	0/0
312	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 2,957.21	2,957.21	1,254.61	07/2005 -	07/2005	-	0/0
313	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91 418.17	418.17	120.30	- -	-	-	0/0
314	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	341.41	272.26	03/2012 03/2013	03/2013	12(O) 0(R)	0/0
315	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,047.00	1,047.00	9.41	- -	-	-	0/0
316	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	302.23	336.49	- -	03/2011	-	0/0
317	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	223.01	108.83	12/2012 -	03/2014	15(O) -	0/0
318	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	925.00	504.78	05/2008 03/2011	03/2011	-	0/0
319	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100007]NCR,Multi State	04/1985	158.77 432.46	540.96	558.07	03/1994 -	12/2011	-	0/0
320	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.98	227.94	202.02	03/2002 -	03/2013	132(O) -	0/0
321	Lumding-SILCHAR Jiribam, Badarpur- Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	4,255.37	3,161.45	03/2009 -	12/2013	57(O) -	0/0
322	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	480.00	0.35	07/2008 -	07/2008	-	0/0
323	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	218.19	162.70	- -	02/2013	- -	0/0
324	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhandd	04/1995	184.00 900.05	900.05	565.12	12/2011 12/2011	03/2013	15(O) 15(R)	0/0

Sector Wise Details

(Aug,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
325	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	791.60	0.76	- -	-	-	0/0
326	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	477.88	392.05	03/2012 03/2013	03/2013	12(O) 0(R)	0/0
327	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	900.00	253.14	- -	-	-	0/0
328	MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N22000093]MRTP,Maharashtra	04/2003	3,125.20 4,174.40	4,501.80	4,334.00	06/2011 03/2012	03/2012	-	0/0
329	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	5,300.00	850.42	03/2014 03/2016	03/2016	24(O) 0(R)	0/0
330	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	645.00	133.87	- -	03/2012	-	0/0
331	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	883.00	626.80	02/2009 -	03/2012	-	0/0
332	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	730.00	347.70	07/2012 07/2012	07/2012	-	0/0
333	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	532.87	39.45	- -	-	-	0/0
334	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 200.00	385.20	112.60	- -	03/2014	-	0/0
335	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 733.00	1,655.81	1,275.88	12/2008 -	03/2014	63(O) -	0/0
336	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	703.17	242.01	- -	03/2015	-	0/0
337	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 850.00	850.00	8.44	03/2015 -	03/2015	0(O) -	0/0
338	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 2,913.51	2,913.51	151.51	03/2016 -	03/2016	0(O) -	0/0
339	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,069.60	27.66	03/2014 03/2016	03/2016	24(O) 0(R)	0/0
340	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	3,951.98	21.71	03/2016 -	03/2016	0(O) -	0/0
341	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 228.82	228.82	32.97	03/2016 -	03/2016	0(O) -	0/0
342	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	1,117.11	-	03/2008 06/2008	-	-	0/0
343	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 -	355.00	401.42	03/2009 12/2009	03/2011	-	0/0
344	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 529.23	529.23	225.10	02/2010 -	12/2015	70(O) -	0/0
345	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 2,921.00	2,921.00	1,514.74	10/2007 12/2012	12/2012	62(O) 0(R)	0/0

Sector Wise Details

(Aug,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestone Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
346	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	925.30	584.06	- -	03/2012	-	0/0
347	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 293.74	293.74	136.74	12/2010 12/2010	12/2010	-	0/0
348	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	1,029.00	753.56	- -	03/2013	- -	0/0
349	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	221.90	231.38	12/2007 03/2010	12/2010	-	0/0
350	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 2,363.00	2,363.00	792.32	03/2009 12/2012	12/2012	45(O) 0(R)	0/0
351	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	243.40	248.79	02/2009 02/2009	04/2013	50(O) 50(R)	0/0
352	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	1,225.00	232.01	- -	-	-	0/0
353	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhandd	04/1997	194.07 194.07	456.45	293.29	06/2004 -	12/2012	102(O) -	0/0
354	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 915.70	1,717.29	1,343.13	- -	03/2013	- -	0/0
355	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	370.00	354.18	04/2003 03/2010	-	-	0/0
356	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	530.76	486.96	02/2010 02/2011	02/2011	-	0/0
357	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94 604.04	639.97	174.53	03/1998 08/2005	08/2005	-	0/0
358	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	482.70	384.35	03/2013 -	03/2014	12(O) -	0/0
359	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 603.04	603.04	96.76	03/2012 -	03/2013	12(O) -	0/0
360	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	385.54	226.12	03/2010 -	03/2012	-	0/0
361	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	3,380.58	52.63	12/2015 -	12/2015	0(O) -	0/0
362	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23 -	818.29	72.97	02/2015 -	-	-	0/0
363	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 516.23	516.23	238.77	03/2014 -	03/2014	0(O) -	0/0
364	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	810.78	113.80	- -	03/2013	-	0/0
365	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	1,086.41	426.22	06/2005 07/2011	06/2016	132(O) 59(R)	0/0
366	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	1,188.91	536.08	- 12/2009	02/2012	-	0/0
367	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 582.83	582.83	129.43	- -	-	-	0/0
368	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 227.40	227.40	36.48	- -	-	-	0/0

Sector Wise Details

(Aug,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
369	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR, Tamil Nadu	09/1995	100.00 100.00	548.96	504.71	- -	-	-	0/0
370	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP, West Bengal	03/2000	907.69 3,176.10	3,176.10	3,205.43	12/2006 08/2010	08/2010	-	0/0
371	Tinpahar - Sahibganj (ER) - [N22000115]ER, Jharkhand	04/2008	167.73 167.73	167.73	46.15	03/2012 -	03/2012	-	0/0
372	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133](NR), J and K	03/1995	2,500.00 2,500.00	8,000.00	8,069.06	03/2001 -	12/2017	201(O) -	0/0
373	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR), Uttar Pradesh	04/2006	325.00 -	820.40	150.01	03/2010 06/2014	06/2014	51(O) 0(R)	0/0
374	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR, Gujarat	04/2008	1,389.62 -	1,389.62	347.99	03/2014 -	03/2013	-12(O) -	0/0
375	VIRAMGAM-BHILDI(WR), GC - [220100062]WR, Multi State	04/1990	155.66 356.87	356.87	166.04	- 03/2010	-	-	0/0
	Total		64,518.68 -	131,959.43	62,072.84				1/1
Road Transport & Highways									
376	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, Bihar	05/2011	351.54 -	351.54	326.19	05/2013 -	03/2014	10(O) -	0/0
377	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI, Bihar	05/2011	511.54 -	511.54	238.72	11/2013 -	11/2013	0(O) -	0/0
378	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, Uttar Pradesh	07/2012	291.36 -	291.36	9.66	01/2014 -	01/2014	0(O) -	0/0
379	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI, Meghalaya	02/2011	226.00 -	226.00	220.00	02/2014 -	02/2014	0(O) -	0/0
380	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, Bihar	05/2011	664.00 -	664.00	211.79	02/2014 -	04/2014	2(O) -	0/0
381	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, Bihar	10/2011	375.09 -	375.09	40.11	04/2014 -	04/2014	0(O) -	0/0
382	2laning with PS Gopalganj-Chappra - [N24000190]NHAI, Bihar	12/2011	325.00 -	325.00	130.53	05/2014 -	05/2014	0(O) -	0/0
383	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI, Multi State	02/2011	2,498.76 -	2,498.76	804.19	08/2014 -	08/2014	0(O) -	0/0
384	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI, Gujarat	12/2010	1,008.50 -	1,008.50	1,097.80	06/2013 -	06/2013	0(O) -	0/0
385	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI, Karnataka	03/2011	359.00 -	359.00	33.82	09/2013 -	07/2014	10(O) -	0/0
386	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI, Gujarat	03/2011	785.50 -	785.50	529.08	08/2013 -	08/2013	0(O) -	0/0
387	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, Bihar	01/2011	575.00 -	575.00	425.81	07/2013 -	07/2013	0(O) -	0/0
388	4-laning of Barhi-Hazaribagh - [N24000191]NHAI, Jharkhand	02/2012	398.00 -	398.00	261.02	02/2014 -	02/2014	0(O) -	0/0
389	4-laning of Brahmapore-Faraka - [N24000203]NHAI, Multi State	02/2011	998.79 -	998.79	530.25	08/2013 -	08/2013	0(O) -	0/0

Sector Wise Details

(Aug,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestone Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
390	4-laning of Faraka-Raiganj - [N24000202]NHAI,Multi State	02/2011	1,078.84	1,078.84	646.48	08/2013	08/2013	0(O)	0/0
391	4-laning of Raiganj-Dalkola - [N24000204]NHAI,Multi State	02/2011	580.43	580.43	218.49	08/2013	08/2013	0(O)	0/0
392	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16	465.50	178.61	09/2007	06/2013	69(O)	0/0
393	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49	367.49	453.68	03/2005	10/2012	91(O)	0/0
394	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00	705.00	1,158.30	11/2012	06/2013	7(O)	0/0
395	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82	221.82	284.81	11/2008	09/2012	46(O)	0/0
396	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00	190.00	259.75	01/2009	12/2012	47(O)	0/0
397	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56	390.56	631.65	02/2012	09/2012	7(O)	0/0
398	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70	228.70	189.38	02/2004	09/2012	103(O)	0/0
399	BAREILY-SITAPUR - [N24000200]NHAI,Uttar Pradesh	03/2011	1,046.00	1,046.00	138.55	09/2013	09/2013	0(O)	0/0
400	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,Rajasthan	12/2011	2,388.00	2,388.00	371.76	06/2014	06/2014	0(O)	0/0
401	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka	12/2010	480.00	480.00	417.00	-	10/2013	-	2/2
402	BHOPAL-SANCHI - [N24000192]NHAI,Madhya pradesh	10/2011	209.00	209.00	3.81	01/2013	10/2013	9(O)	0/0
403	BHUBANESWAR TO PURI - [N24000195]NHAI,Orissa	03/2011	500.29	500.29	380.32	08/2013	08/2013	0(O)	0/0
404	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80	237.80	248.21	06/2008	12/2012	54(O)	0/0
405	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00	195.00	205.46	06/2008	03/2013	57(O)	0/0
406	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00	230.00	226.35	06/2005	09/2012	87(O)	0/0
407	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61	217.61	212.06	04/2010	12/2012	32(O)	0/0
408	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00	281.31	179.23	02/2010	12/2013	46(O)	0/0
409	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00	852.00	667.28	03/2013	03/2013	0(O)	0/0
410	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,Karnataka	03/2011	839.00	839.00	302.14	-	12/2013	-	0/1
411	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00	1,585.00	957.76	05/2013	05/2013	0(O)	0/0
412	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37	353.37	355.53	10/2011	03/2014	29(O)	0/0

Sector Wise Details

(Aug,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
413	Chilkaluript-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30	572.30	691.40	10/2011	06/2013	20(O)	0/0
414	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00	225.00	281.21	06/2008	12/2012	54(O)	0/0
415	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00	300.00	175.01	10/2008	03/2014	65(O)	0/0
416	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00	486.00	587.32	05/2010	12/2012	31(O)	0/0
417	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	953.00	593.00	371.11	07/2013	07/2013	0(O)	0/0
418	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu	06/2011	600.00	600.00	75.85	06/2013	06/2013	0(O)	0/0
419	DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka	12/2010	453.00	453.00	351.33	-	06/2013	-	1/1
420	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00	200.00	231.15	06/2008	03/2013	57(O)	0/0
421	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00	160.00	175.99	05/2008	03/2013	58(O)	0/0
422	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45	232.45	274.33	09/2010	12/2012	27(O)	0/0
423	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00	485.00	72.63	08/2013	08/2013	0(O)	0/0
424	END OF DURG BYPASS- CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI,Chhatisgarh	01/2008	464.00	464.00	535.25	01/2011	12/2012	23(O)	0/0
425	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94	332.94	389.13	09/2008	12/2012	51(O)	0/0
426	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52	1,170.52	4.41	06/2011	10/2012	16(O)	0/0
427	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00	201.66	128.88	09/2008	03/2013	54(O)	0/0
428	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27	263.27	269.79	02/2004	09/2012	103(O)	0/0
429	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI,Uttar Pradesh	12/2003	275.00	275.00	306.19	09/2007	09/2012	60(O)	0/0
430	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00	1,141.00	679.81	08/2013	08/2013	0(O)	0/0
431	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16	198.16	210.81	04/2008	12/2012	56(O)	0/0
432	GUWAHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96	175.96	151.42	04/2008	12/2012	56(O)	0/0
433	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93	300.93	302.72	10/2009	12/2012	38(O)	0/0
434	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00	604.00	494.29	12/2009	12/2012	36(O)	0/0

Sector Wise Details

(Aug,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestone Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
435	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10	1,509.10	1,427.90	09/2012	09/2012	0(O)	0/0
436	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70	1,673.70	2,723.00	10/2011	12/2012	14(O)	0/0
437	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00	220.00	277.83	09/2007	09/2012	60(O)	0/0
438	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00	280.00	271.25	02/2009 05/2014	05/2013	51(O) -12(R)	0/0
439	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00	363.74	49.25	07/2009	04/2014	57(O)	0/0
440	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00	386.10	26.30	09/2007	03/2013	66(O)	0/0
441	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00	207.56	185.13	08/2004	10/2012	98(O)	0/0
442	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00	196.65	179.66	08/2004 07/2010	10/2012	98(O) 27(R)	0/0
443	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhand	08/2010	625.07	625.07	857.54	01/2013	01/2013	0(O)	0/0
444	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI,Karnataka	09/2010	946.00	946.00	1,394.40	-	03/2013	-	3/3
445	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI,Andhra Pradesh	04/2010	1,740.00	1,740.00	1,848.50	10/2012	10/2012	0(O)	0/0
446	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI,Andhra Pradesh	08/2010	388.00	388.00	506.40	05/2012	09/2012	4(O)	0/0
447	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00	325.00	376.84	05/2013	02/2014	9(O)	0/0
448	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh	10/2010	1,175.00	1,175.00	138.67	04/2013	04/2013	0(O)	0/0
449	JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan	08/2010	267.81	267.81	521.08	02/2013	02/2013	0(O)	0/0
450	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,J and K	07/2010	1,813.76	1,813.76	-	07/2013	06/2014	11(O)	0/0
451	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar	12/2003	340.00	340.00	541.94	09/2008	12/2012	51(O)	0/0
452	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06	355.06	469.55	09/2009	12/2012	39(O)	0/0
453	JORBAT - BARAPANI - [N24000180]NHAI,Meghalaya	01/2011	536.00	536.00	387.88	01/2014	01/2014	0(O)	0/0
454	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06	792.06	1,387.70	12/2012	12/2012	0(O)	0/0
455	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00	250.39	279.36	10/2008	09/2012	47(O)	0/0
456	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00	240.00	294.12	10/2008	03/2013	53(O)	0/0
457	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,West Bengal	02/2012	702.16	702.16	150.41	07/2014	07/2014	0(O)	0/0

Sector Wise Details

(Aug,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
458	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,Karnataka	09/2010	671.00	671.00	737.54	-	03/2013	-	2/3
459	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00	795.00	1,023.40	05/2012	09/2012	4(O)	0/0
460	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60	407.60	185.78	06/2010	10/2012	28(O)	0/0
461	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17	263.17	233.77	09/2009	09/2014	60(O)	0/0
462	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04	280.13	92.32	11/2008	07/2013	56(O)	0/0
463	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81	385.13	60.42	04/2009	07/2013	51(O)	0/0
464	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64	167.64	20.73	11/2008	01/2014	62(O)	0/0
465	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00	200.00	112.26	04/2009	03/2013	47(O)	0/0
466	MP/Maharashtra Border-Dhula - [N24000126]NHAI,Maharashtra	12/2009	835.00	835.00	1,068.70	06/2012	12/2012	6(O)	0/0
467	MURADABAD-BAREILY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00	1,267.00	1,264.30	06/2013	06/2013	0(O)	0/0
468	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,Multi State	09/2011	754.00	754.00	384.91	03/2013	03/2013	0(O)	0/0
469	Muzafarpur - Sonbarsa - [N24000174]NHAI,Bihar	05/2011	511.54	511.54	238.72	11/2013	11/2013	0(O)	0/0
470	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72	264.72	287.76	06/2008	03/2013	57(O)	0/0
471	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00	168.00	457.30	12/2008	12/2012	48(O)	0/0
472	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,Maharashtra	04/2012	484.19	484.19	-	10/2014	10/2014	0(O)	0/0
473	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00	208.00	266.19	04/2008	12/2012	56(O)	0/0
474	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00	225.00	240.75	06/2008	03/2013	57(O)	0/0
475	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00	200.00	274.19	06/2008	12/2012	54(O)	0/0
476	NASHRI CHANANI - [N24000162]NHAI,J and K	06/2010	2,159.00	2,159.00	-	06/2015	05/2016	11(O)	0/0
477	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50	196.50	248.66	06/2011	12/2012	18(O)	0/2
478	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00	557.00	930.92	02/2010	12/2014	58(O)	0/0
479	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,Orissa	07/2011	586.00	586.00	237.55	01/2014	01/2014	0(O)	0/0
480	New 4 Lane elevated road from chennai airport - [N24000139]NHAI,Tamil Nadu	09/2010	1,655.00	1,655.00	426.98	09/2013	09/2013	0(O)	0/0

Sector Wise Details

(Aug,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
481	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68 -	340.68	385.28	03/2008 -	12/2012	57(O) -	0/0
482	PANIKHOLI-RIMOLI - [N24000197]NHAI,Orissa	03/2012	1,410.00 -	1,410.00	148.10	09/2014 -	09/2014	0(O) -	0/0
483	PANIPAT-ROHTAK - [N24000151]NHAI,Haryana	04/2011	807.00 -	807.00	884.84	10/2014 -	10/2014	0(O) -	0/0
484	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	359.00	216.44	05/2008 -	03/2013	58(O) -	0/0
485	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,Bihar	09/2011	574.00 -	574.00	403.96	03/2014 -	03/2014	0(O) -	0/0
486	PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar	08/2010	671.30 -	671.30	586.44	02/2013 -	02/2013	0(O) -	0/0
487	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00 -	940.00	1,141.10	07/2012 -	12/2012	5(O) -	0/0
488	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55 -	1,724.55	975.44	03/2013 -	03/2013	0(O) -	0/0
489	PUNE-SHOLAPUR,Pkg-II - [N24000193]NHAI,Maharashtra	09/2011	835.00 -	835.00	104.67	01/2014 -	01/2014	0(O) -	0/0
490	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00 -	2,288.00	3,460.60	11/2011 -	08/2013	21(O) -	0/0
491	Pune-sholapur,pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00 -	1,110.00	1,802.10	05/2012 -	10/2013	17(O) -	0/0
492	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,J and K	07/2010	1,987.00 -	1,987.00	-	07/2015 -	06/2016	11(O) -	0/0
493	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	251.03	309.92	10/2008 -	12/2012	50(O) -	0/0
494	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI,Madhya pradesh	12/2003	229.91 -	229.91	262.25	10/2008 -	12/2012	50(O) -	0/0
495	ROHTAK-BAWAL - [N24000169]NHAI,Haryana	05/2011	650.00 -	650.00	734.10	11/2013 -	11/2013	0(O) -	0/0
496	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI, Madhya pradesh	12/2003	203.43 -	203.43	237.75	10/2008 -	12/2012	50(O) -	0/0
497	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI,Uttar Pradesh	12/2003	151.30 -	151.30	190.52	10/2008 -	10/2012	48(O) -	0/0
498	SALEM - U / UNDRUPET(BOT -1/TN-06) NH - 68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00 -	941.00	1,901.00	01/2011 -	02/2013	25(O) -	0/0
499	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,Gujarat	09/2010	805.39 -	805.39	308.07	03/2013 -	03/2013	0(O) -	0/0
500	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,Orissa	11/2011	909.00 -	909.00	844.05	05/2014 -	05/2014	0(O) -	0/0
501	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47 -	154.57	201.65	09/2007 -	03/2013	66(O) -	0/0
502	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	225.00	183.84	07/2008 -	12/2012	53(O) -	0/0

Sector Wise Details

(Aug,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original /Revised (in months)	Milestones Achieved/ Total	
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	
503	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI,Tamil Nadu	06/2011	535.00 -	535.00	-	12/2013 -	12/2013	0(O) -	0/0	
504	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM. - [N24000172]NHAI,Tamil Nadu	09/2011	1,250.00 -	1,250.00	12.48	12/2013 -	12/2013	0(O) -	0/0	
505	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI,Andhra Pradesh	11/2011	1,535.00 -	1,535.00	822.95	05/2014 -	05/2014	0(O) -	0/0	
506	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00 -	617.00	154.52	08/2012 -	03/2014	19(O) -	0/0	
507	SNG toBANL - [N24000189]NHAI,J and K	06/2011	1,100.70 -	1,100.70	-	06/2014 -	06/2014	0(O) -	0/0	
508	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00 -	245.00	491.21	03/2008 -	03/2013	60(O) -	0/0	
509	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00 -	241.53	132.10	04/2004 -	09/2012	101(O) -	0/0	
510	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75 -	1,693.75	2,659.00	08/2011 -	10/2012	14(O) -	0/0	
511	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	280.00	581.49	06/2009 -	11/2012	41(O) -	0/0	
512	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00 -	516.00	760.07	07/2010 -	03/2013	32(O) -	0/0	
513	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00 -	567.00	471.21	11/2013 -	11/2013	0(O) -	0/0	
514	Tirupati - Chennai - [N24000178]NHAI,Tamil Nadu	04/2011	571.00 -	571.00	-	10/2013 -	10/2013	0(O) -	0/0	
515	Trichy Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00 -	374.00	75.23	05/2013 -	05/2013	0(O) -	0/0	
516	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00 -	680.00	99.39	- -	04/2013	- -	2/2	
517	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,Multi State	09/2011	2,848.00 -	2,848.00	677.05	03/2014 -	03/2014	0(O) -	0/0	
518	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J and K	12/2003	166.27 -	193.10	163.41	03/2008 -	10/2012	55(O) -	0/0	
519	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45 -	193.45	31.47	11/2012 -	11/2012	0(O) -	0/0	
520	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88 -	953.88	386.37	07/2013 -	07/2013	0(O) -	0/0	
521	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]NHAI,Multi State	12/2011	1,047.00 -	1,047.00	148.11	06/2014 -	06/2014	0(O) -	0/0	
Total			92,448.72	94,027.34	66,341.65					10/14

Shipping & Ports

Sector Wise Details

(Aug,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
522	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	359.44	358.78	04/2011 10/2012	10/2012	18(O) 0(R)	0/0
523	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91 -	968.35	777.97	09/2012 -	09/2012	0(O) -	0/0
524	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 627.64	627.64	214.65	12/2012 05/2013	05/2013	5(O) 0(R)	0/0
525	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	277.03	188.88	12/2011 09/2012	09/2012	9(O) 0(R)	0/0
526	Acquisition of two nos. of 120 B.P BY 079& 080 - [N25000042]SHIPP.,Maharashtra	04/2009	290.85 -	305.00	197.14	06/2011 09/2012	09/2012	15(O) 0(R)	0/0
527	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	994.82	248.23	02/2014 -	02/2014	0(O) -	0/0
528	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	1,028.10	371.96	12/2013 -	10/2013	-2(O) -	0/0
529	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	841.40	12/2010 09/2012	10/2013	34(O) 13(R)	0/0
530	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	24(O) -	0/0
531	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012	22(O) -	0/0
532	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 1,571.60	1,571.60	5.75	10/2008 -	10/2008	-	0/0
533	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84 -	253.36	-	- 01/2009	01/2009	-	0/1
534	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 600.00	600.00	110.00	03/2006 06/2013	06/2013	87(O) 0(R)	0/0
535	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	29(O) -	0/0
536	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	277.00	0.21	03/2012 -	03/2012	-	0/0
537	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	373.22	326.08	04/2009 11/2009	02/2011	-	0/0
538	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	2,427.40	829.43	10/2008 -	-	-	0/0
539	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	4,150.00	3,433.40	01/2012 09/2012	12/2012	11(O) 3(R)	0/0
540	Setting up of Single Point Mooring (SPM) and allie - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -	621.53	-	05/2013 -	03/2013	-2(O) -	0/0

Sector Wise Details

(Aug,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	Total		16,242.52	18,554.09	8,123.81				0/1
	<u>Telecommunications</u>								
541	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81	336.81	157.98	01/2009	03/2013	50(O)	0/0
542	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00	247.00	75.89	02/2007 12/2010	-	-	0/0
543	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	229.41	67.20	02/2007 03/2012	02/2013	72(O) 11(R)	0/0
544	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00	384.00	29.45	10/2010 03/2012	03/2013	29(O) 12(R)	0/0
545	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38	168.30	-	10/2007	-	-	0/0
546	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00	1,077.00	-	03/2009	-	-	0/0
547	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	158.72	76.70	06/2009	12/2012	42(O)	0/0
548	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94	373.94	231.79	12/2008	12/2012	48(O)	0/0
549	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 930.60	930.60	805.75	11/2010	11/2012	24(O)	0/0
550	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84	336.84	35.75	10/2009	03/2011	-	0/0
551	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL,Jharkhandd	03/2008	328.13	328.12	164.58	03/2009	12/2012	45(O)	0/0
552	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65	152.65	-	03/2010	-	-	0/0
553	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88	952.88	-	03/2010	-	-	0/0
554	NIB Project Capacity Expansion - [N26000098]BSNL,Multi State	06/2007	175.52	175.52	60.84	12/2008	11/2012	47(O)	0/0
555	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00	250.00	80.47	12/2005 03/2008	11/2012	83(O) 56(R)	0/0
	Total		6,161.00	6,101.79	1,786.40				0/0
	<u>Urban Development</u>								
556	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00	11,609.00	2,267.57	12/2011	03/2013	15(O)	6/6
557	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	173.08	-	04/2009	-	-	0/0
558	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00	35,242.00	709.91	03/2016	03/2016	0(O)	0/0

Sector Wise Details

(Aug,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
559	FARIDABAD EXTENSION - [N28000057]DMRC, Delhi	09/2011	2,494.00	2,494.00	69.58	09/2014	09/2014	0(O)	0/0
			-			-		-	
	Total		44,245.18	49,518.08	3,047.06				6/6
			-						
<u>Water Resources</u>									
560	PAGLADIYA DAM PROJECT - [300100001]MoWR, Assam	01/2001	542.90	1,187.00	35.49	12/2007	12/2012	60(O)	0/0
			-			-		-	
	Total		542.90	1,187.00	35.49				0/0
			-						
Grand Total			765,702.99	883,467.92	412,178.56				899/3228


Summary of projects in the Flash Report for the month of August, 2012

I. Project Implementation - Current Status:

Number of Projects in Previous Month	560
Number of Projects completed/dropped/frozen in Previous Month	2
Number of Projects completed/dropped/frozen in Current Month	6
Number of Projects Removed From the System in Current Month	1
Number of Projects Added in Current Month	9
Number of Projects in Current Month	560


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 560 projects, 5 projects are ahead of schedule, 167 projects are on schedule and 272 projects are delayed. Of the balance, 83 projects do not have fixed dates of commissioning while 33 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

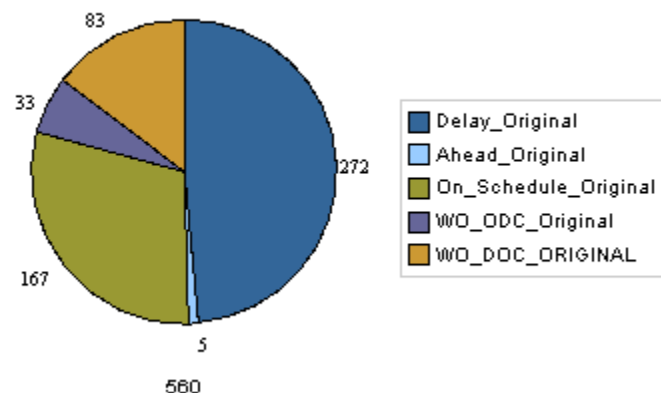

III. Investment Scenario

The Total Original cost of implementation of 560 projects when sanctioned, was of the order of Rs. 765702.99 crore but this was subsequently revised to Rs. 883467.92 crore implying a cost overrun of 15.4%. The expenditure incurred on these projects till August, 2012 is Rs. 412178.56 crore, which is 46.7% of the revised cost of the projects.

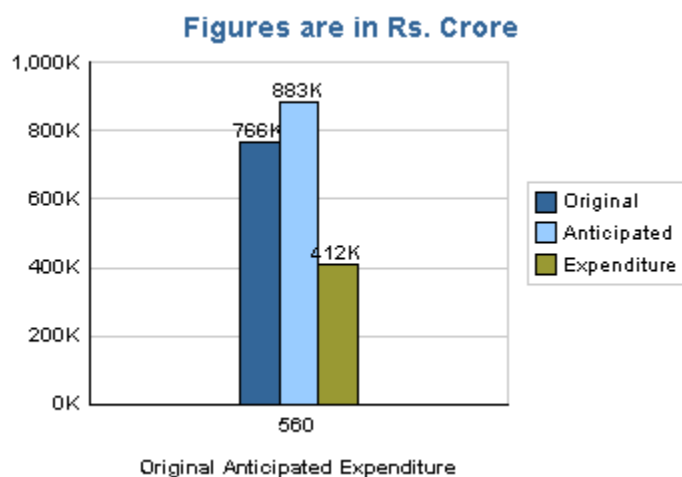

Sector wise current status of projects on theFlash Report

Urban Development


I. Current Status:

Number of Projects	4
Number of Projects On Schedule	2
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 2 projects are on schedule and 1 project are delayed .1 project do not have fixed dates of commissioning.

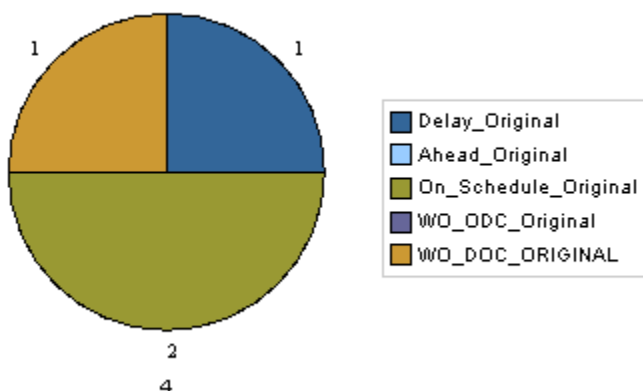

III. Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 44245.18 crore but this was subsequently revised to Rs. 49518.08 crore implying a cost overrun of 11.9%. The expenditure incurred on these projects till August, 2012 is Rs. 3047.06 crore, which is 6.2% of the revised cost of the projects.

Figures are in Rs. Crore

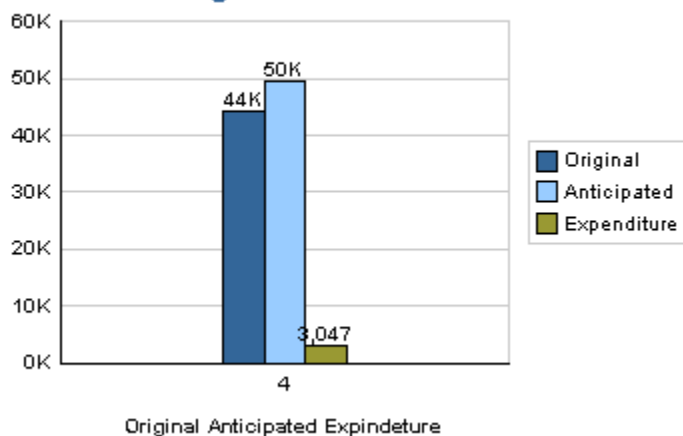

Sector wise current status of projects on theFlash Report

Telecommunications

I. Current Status:


Number of Projects **15**

Number of Projects Delayed **9**

Number of Projects Without Date Of Commissioning **6**

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 15 projects, 9 projects are delayed .6 projects do not have fixed dates of commissioning.

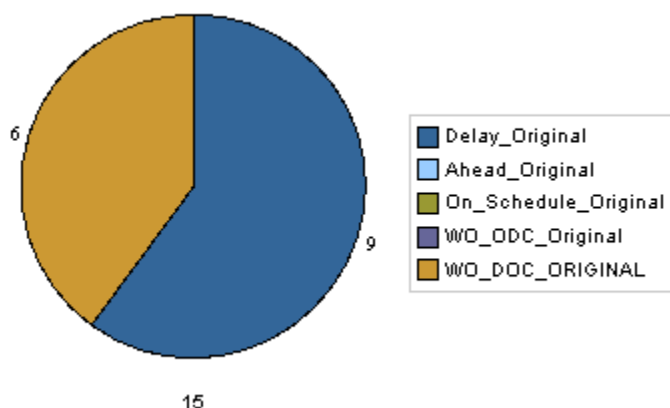

III. Investment Scenario

The Total Original cost of implementation of 15 projects when sanctioned, was of the order of Rs. 6161 crore but this was subsequently revised to Rs. 6101.79 crore implying a cost overrun of -1%. The expenditure incurred on these projects till August, 2012 is Rs. 1786.4 crore, which is 29.3% of the revised cost of the projects.

Figures are in Rs. Crore

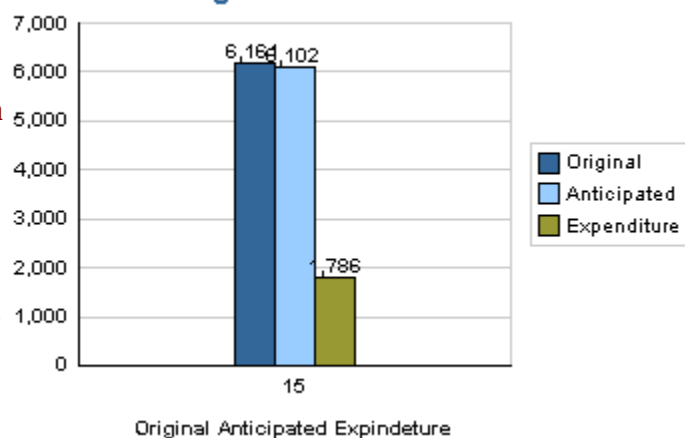

Sector wise current status of projects on theFlash Report


Shipping & Ports

I. Current Status:

Number of Projects	19
Number of Projects On Schedule	2
Number of Projects Delayed	10
Number of Projects Ahead	2
Number of Projects Without Date Of Commissioning	5

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 19 projects, 2 projects are ahead of schedule, 2 projects are on schedule and 10 projects are delayed .5 projects do not have fixed dates of commissioning.

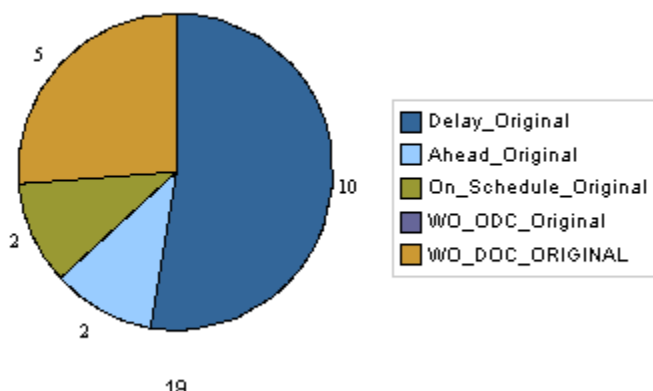

III. Investment Scenario

The Total Original cost of implementation of 19 projects when sanctioned, was of the order of Rs. 16242.52 crore but this was subsequently revised to Rs. 18554.09 crore implying a cost overrun of 14.2%. The expenditure incurred on these projects till August, 2012 is Rs. 8123.81 crore, which is 43.8% of the revised cost of the projects.

Figures are in Rs. Crore

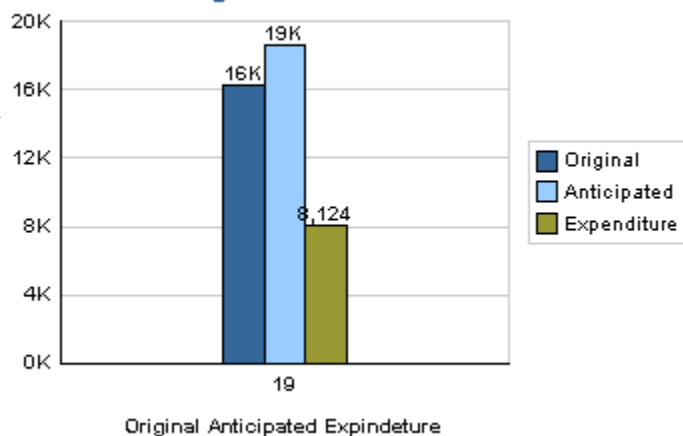

Sector wise current status of projects on theFlash Report

Road Transport & Highways


I. Current Status:

Number of Projects	146
Number of Projects On Schedule	56
Number of Projects Delayed	84

Number of Projects Without Original Date of Commissioning	6
---	---


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 146 projects, 56 projects are on schedule and 84 projects are delayed .6 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

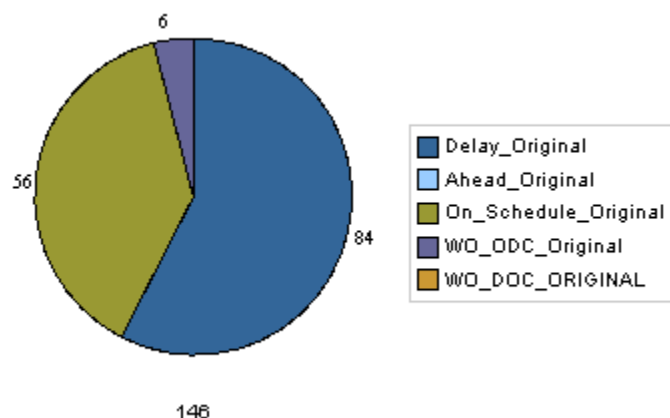

III. Investment Scenario

The Total Original cost of implementation of 146 projects when sanctioned, was of the order of Rs. 92448.72 crore but this was subsequently revised to Rs. 94027.34 crore implying a cost overrun of 1.7%. The expenditure incurred on these projects till August, 2012 is Rs. 66341.65 crore, which is 70.6% of the revised cost of the projects.

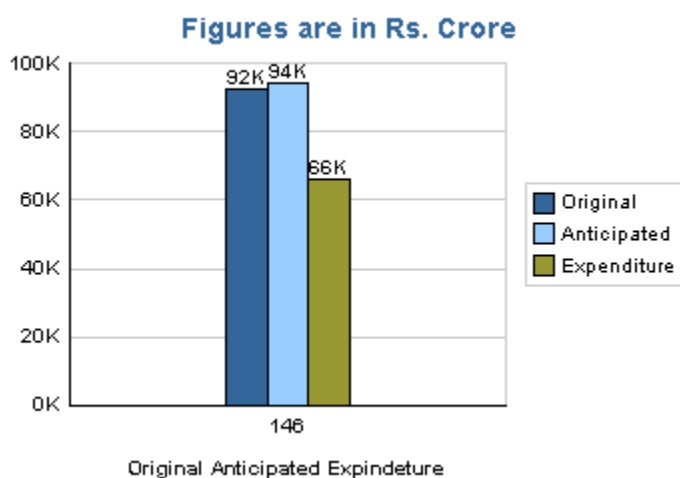

Sector wise current status of projects on theFlash Report


Railways

I. Current Status:

Number of Projects	127
Number of Projects On Schedule	10
Number of Projects Delayed	39
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	18
Number of Projects Without Date Of Commissioning	59

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 127 projects, 1 project are ahead of schedule, 10 projects are on schedule and 39 projects are delayed .59 projects do not have fixed dates of commissioning.18 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

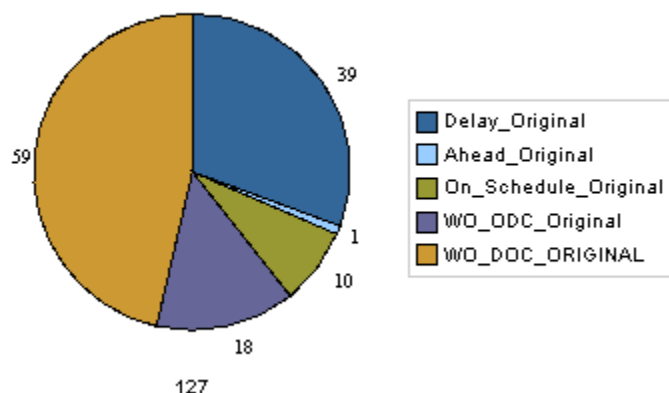

III. Investment Scenario

The Total Original cost of implementation of 127 projects when sanctioned, was of the order of Rs. 64518.68 crore but this was subsequently revised to Rs. 131959.43 crore implying a cost overrun of 104.5%. The expenditure incurred on these projects till August, 2012 is Rs. 62072.84 crore, which is 47% of the revised cost of the projects.

Figures are in Rs. Crore

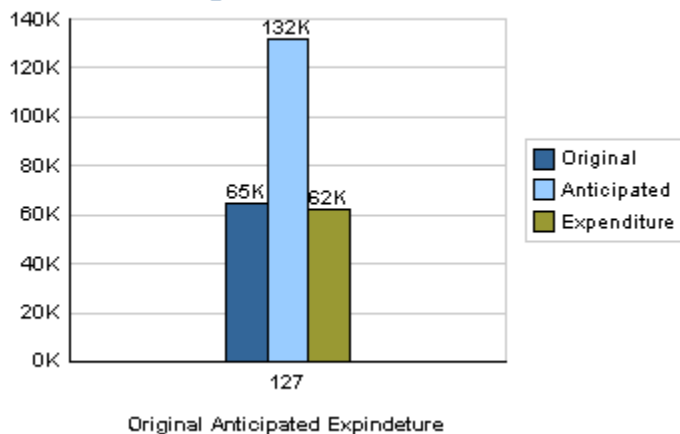

Sector wise current status of projects on theFlash Report

Power


I. Current Status:

Number of Projects	94
Number of Projects On Schedule	42
Number of Projects Delayed	48

Number of Projects Without Original Date of Commissioning	2
Number of Projects Without Date Of Commissioning	2

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 94 projects, 42 projects are on schedule and 48 projects are delayed .2 projects do not have fixed dates of commissioning.2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

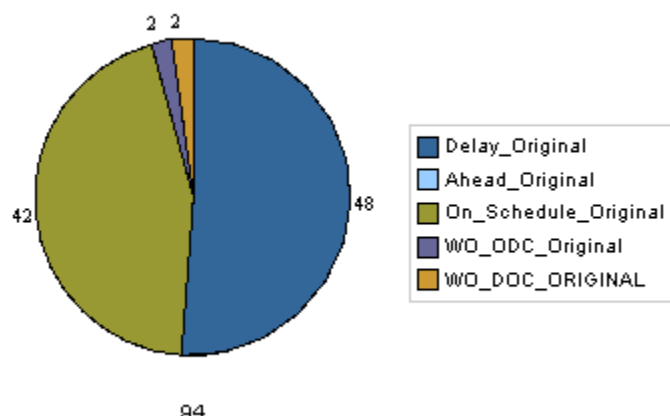

III. Investment Scenario

The Total Original cost of implementation of 94 projects when sanctioned, was of the order of Rs. 224936.05 crore but this was subsequently revised to Rs. 238936.53 crore implying a cost overrun of 6.2%. The expenditure incurred on these projects till August, 2012 is Rs. 101520.58 crore, which is 42.5% of the revised cost of the projects.

Figures are in Rs. Crore

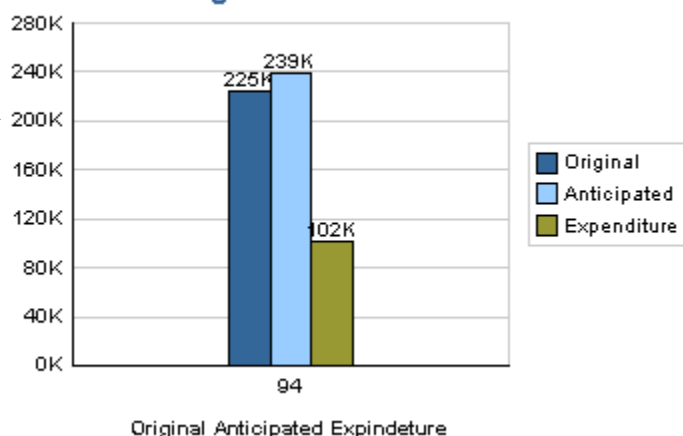

Sector wise current status of projects on theFlash Report

Petroleum


I. Current Status:

Number of Projects	69
Number of Projects On Schedule	21
Number of Projects Delayed	39

Number of Projects Without Original Date of Commissioning	5
Number of Projects Without Date Of Commissioning	4

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 69 projects, 21 projects are on schedule and 39 projects are delayed .4 projects do not have fixed dates of commissioning.5 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

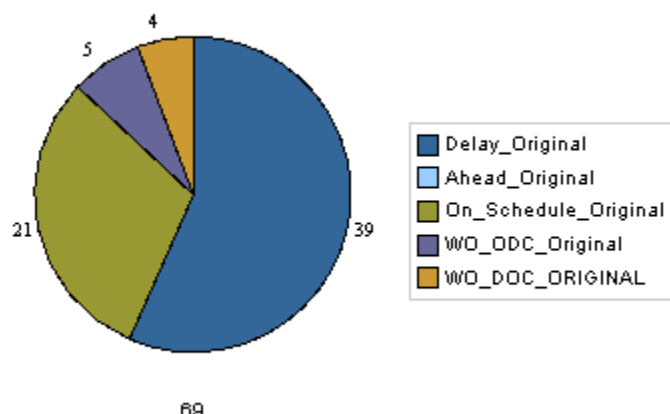

III. Investment Scenario

The Total Original cost of implementation of 69 projects when sanctioned, was of the order of Rs. 157954.47 crore but this was subsequently revised to Rs. 166783.98 crore implying a cost overrun of 5.6%. The expenditure incurred on these projects till August, 2012 is Rs. 79387.86 crore, which is 47.6% of the revised cost of the projects.

Figures are in Rs. Crore

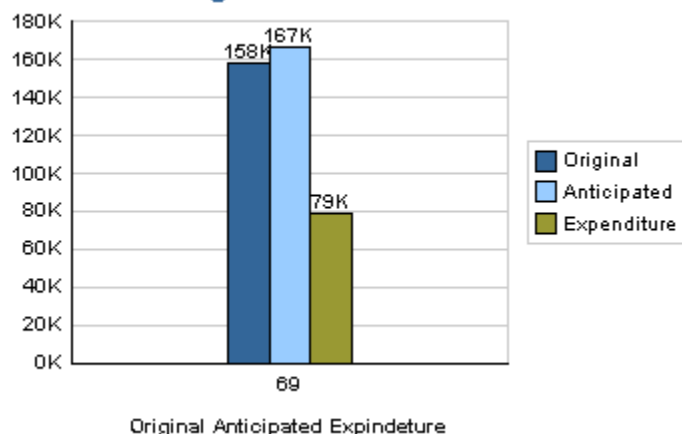

Sector wise current status of projects on theFlash Report


Steel

I. Current Status:

Number of Projects	17
Number of Projects On Schedule	3
Number of Projects Delayed	11
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	2

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 17 projects, 1 project are ahead of schedule, 3 projects are on schedule and 11 projects are delayed .2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

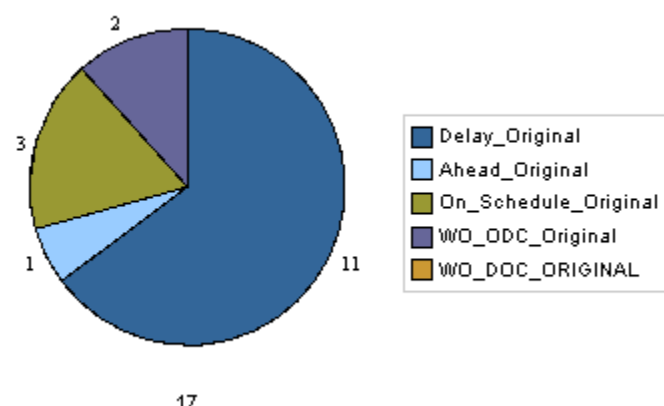

III. Investment Scenario

The Total Original cost of implementation of 17 projects when sanctioned, was of the order of Rs. 65285.87 crore but this was subsequently revised to Rs. 71443.41 crore implying a cost overrun of 9.4%. The expenditure incurred on these projects till August, 2012 is Rs. 42455.98 crore, which is 59.4% of the revised cost of the projects.

Figures are in Rs. Crore

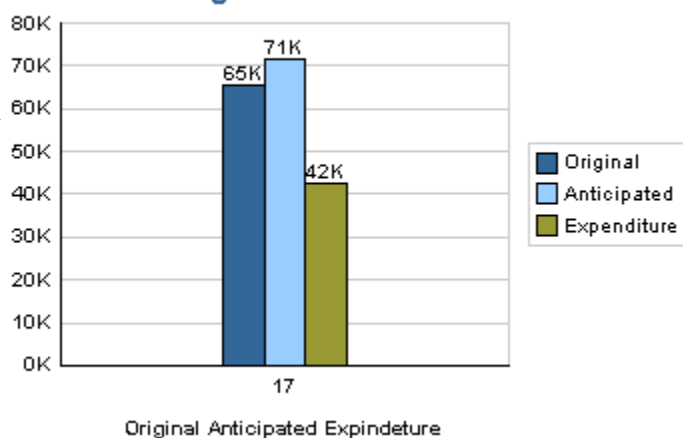

Sector wise current status of projects on theFlash Report


Fertilisers

I. Current Status:

Number of Projects	5
Number of Projects On Schedule	2
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	2

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 5 projects, 1 project are ahead of schedule, 2 projects are on schedule and 2 projects do not have fixed dates of commissioning.

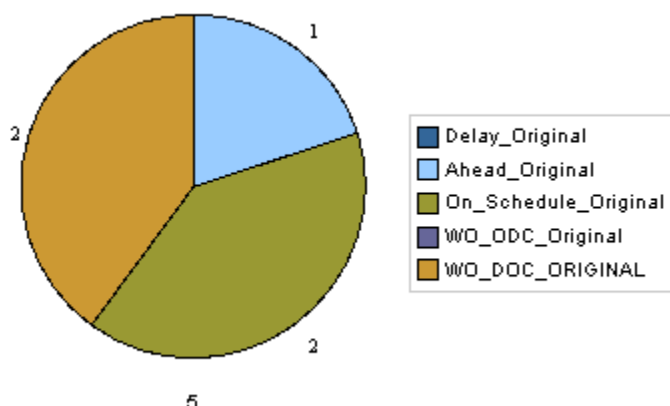

III. Investment Scenario

The Total Original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 4828.66 crore but this was subsequently revised to Rs. 4828.66 crore implying a cost overrun of 0%. The expenditure incurred on these projects till August, 2012 is Rs. 2453.98 crore, which is 50.8% of the revised cost of the projects.

Figures are in Rs. Crore

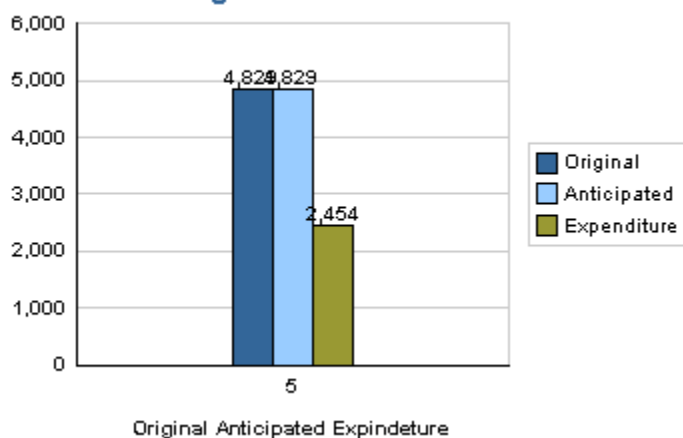

Sector wise current status of projects on theFlash Report

Coal


I. Current Status:

Number of Projects	51
Number of Projects On Schedule	26
Number of Projects Delayed	24

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 51 projects, 26 projects are on schedule and 24 projects are delayed .1 project do not have fixed dates of commissioning.

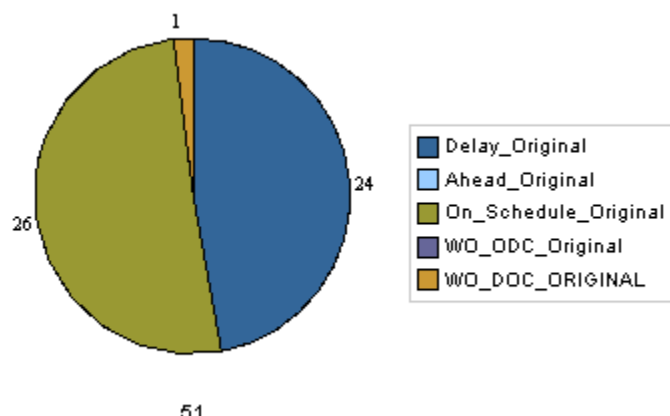

III. Investment Scenario

The Total Original cost of implementation of 51 projects when sanctioned, was of the order of Rs. 36056.46 crore but this was subsequently revised to Rs. 37312.25 crore implying a cost overrun of 3.5%. The expenditure incurred on these projects till August, 2012 is Rs. 12653.88 crore, which is 33.9% of the revised cost of the projects.

Figures are in Rs. Crore

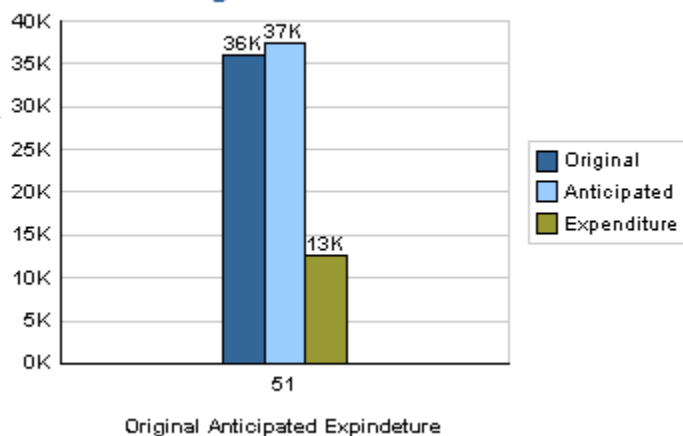

Sector wise current status of projects on theFlash Report

Civil Aviation


I. Current Status:

Number of Projects	6
Number of Projects On Schedule	2
Number of Projects Delayed	3

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 6 projects, 2 projects are on schedule and 3 projects are delayed .1 project do not have fixed dates of commissioning.

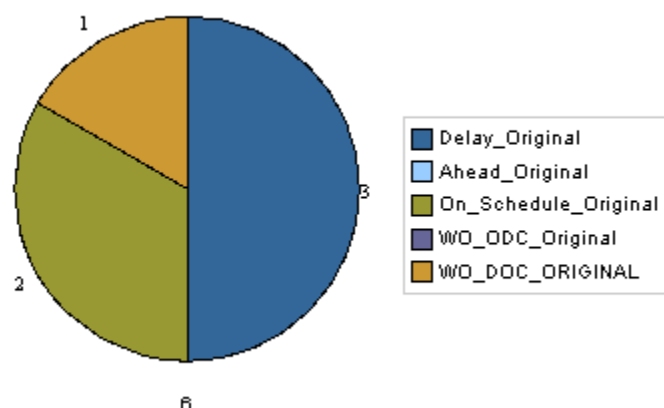

III. Investment Scenario

The Total Original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 5473.58 crore but this was subsequently revised to Rs. 6063.07 crore implying a cost overrun of 10.8%. The expenditure incurred on these projects till August, 2012 is Rs. 4446.95 crore, which is 73.3% of the revised cost of the projects.

Figures are in Rs. Crore

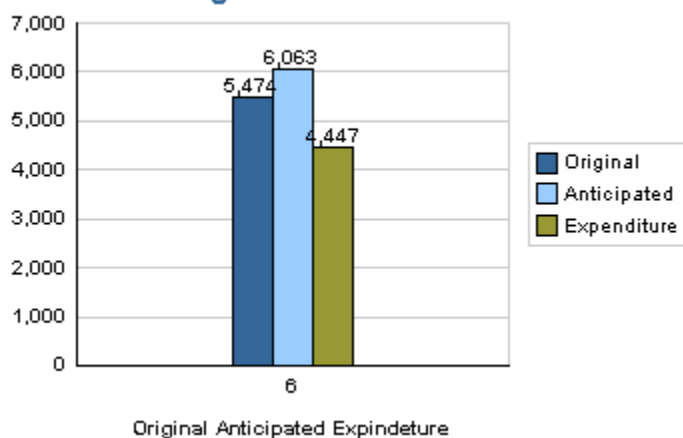

Sector wise current status of projects on theFlash Report

Atomic Energy

I. Current Status:


Number of Projects 5

Number of Projects Delayed 3

Number of Projects Without Date Of Commissioning 2

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 5 projects, 3 projects are delayed .2 projects do not have fixed dates of commissioning.

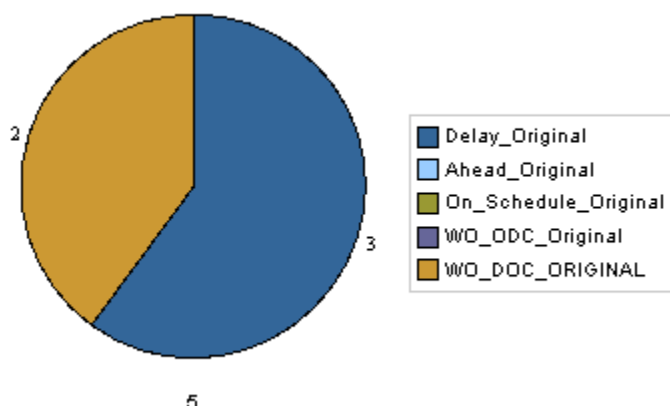

III. Investment Scenario

The Total Original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 41548.29 crore but this was subsequently revised to Rs. 47832.29 crore implying a cost overrun of 15.1%. The expenditure incurred on these projects till August, 2012 is Rs. 22654.84 crore, which is 47.4% of the revised cost of the projects.

Figures are in Rs. Crore

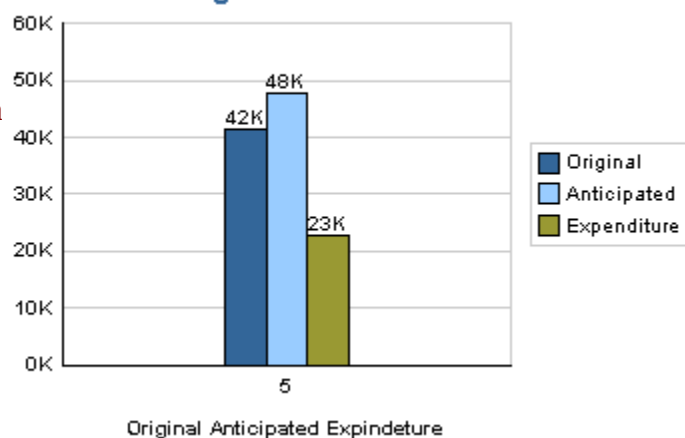

ANNEXURES

CENTRAL SECTOR PROJECTS AS ON 01.09.2012

SN	STATE_NAME	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMMULATIVE EXPENDITURE
1	Andhra Pradesh	36	31031.62	38459.02	22194.50
2	Arunachal Pr.	4	9512.22	14153.62	8312.76
3	Assam	36	22463.87	34047.36	22202.26
4	Bihar	30	26901.24	34657.03	22050.99
5	Chhatisgarh	24	46715.19	47998.27	13394.87
6	Delhi	5	38572.55	38552.96	846.69
7	Goa	1	335.61	335.61	130.41
8	Gujarat	22	31111.55	31313.49	8206.32
9	Haryana	10	5496.60	7367.17	7357.06
10	Himachal Pr.	5	13355.57	15414.93	12377.65
11	J and K	10	14926.96	22827.56	13172.86
12	Jharkhandd	22	14293.58	18275.16	7686.88
13	Karnataka	24	44634.83	52983.83	19724.05
14	Kerala	5	5469.67	6911.22	4941.88
15	Madhya pradesh	23	16561.52	16855.99	8840.55
16	Maharashtra	55	96485.62	111451.94	51383.56
17	Manipur	1	727.56	4444.00	911.23
18	Meghalaya	2	762.00	762.00	607.88
19	Mizoram	2	1532.97	3307.11	356.19
20	Multi State	101	135603.18	141284.31	62436.55
21	Nagaland	1	850.00	850.00	8.44
22	Orissa	30	57409.06	61398.87	32059.77
23	Punjab	7	4836.20	5777.97	3842.89
24	Rajasthan	14	26544.10	26138.31	9059.56
25	Sikkim	2	1648.94	3690.04	237.81
26	Tamil Nadu	32	51275.95	62055.82	38825.99
27	Tripura	3	1522.39	2053.23	886.91
28	Uttar Pradesh	24	18613.30	22451.07	11592.12
29	Uttaranchal	3	5619.21	6559.64	1920.95
30	West Bengal	26	40889.93	51090.39	26608.98
TOTAL		560	765702.99	883467.92	412178.56

List of projects in which Expenditure more than cost as on 31-08-2012

SN	PROJECT	AGENCY	SECTOR	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	Atomic Energy	3492.00	0.00	3641.60
2	KUDANKULAM APP (NPCIL)	NPCIL	Atomic Energy	13171.00	0.00	14945.00
3	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT	AAI	Civil Aviation	1942.51	0.00	2081.48
4	RESITMENT OF MARKETING INSTALATION AT VISAKH	HPCL	Petroleum	756.00	0.00	893.30
5	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC)	NHPC	Power	768.92	0.00	1551.34
6	TEESTA LOW DAM HEP, STAGE-IV (NHPC)	NHPC	Power	1061.38	0.00	1173.29
7	CHUTAK HYDRO-ELECTRIC PROJECT	NHPC	Power	621.26	0.00	751.21
8	NIMOO BAZGO HYDROELECTRIC PROJECT	NHPC	Power	611.01	0.00	786.38
9	URI H.E.P STAGE -II (NHPC)	NHPC	Power	1729.29	0.00	1772.30
10	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP	PGCIL	Power	557.24	0.00	589.00
11	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	(NR)	Railways	2500.00	2500.00	8069.06
12	CHANDIGARH-LUDHIANA(NEW BG LINE),NR	(NR)	Railways	248.44	576.27	877.21
13	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	(NR)	Railways	409.00	625.30	833.20
14	REWARI-ROHTAK (NL),NR	(NR)	Railways	149.38	330.23	486.96
15	JIND-SONEPAT (NL),NR	(NR)	Railways	190.81	238.56	414.03
16	AMRAVATI-NARKHER NL(CR)	CR	Railways	120.90	405.17	518.45
17	LANJHIGARH-JUNAGARH NL(ECOR)	ECOR	Railways	100.00	142.98	202.02
18	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	ECR	Railways	233.00	501.69	659.06
19	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	Railways	114.01	332.92	392.05
20	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara and Noapara-NSCB Airport(MTP)	M RTP	Railways	907.69	3176.10	3205.43
21	MUMBAI URBAN TRANSPORT PROJECT PHASE-I	M RTP	Railways	3125.20	4174.40	4334.00
22	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	NCR	Railways	158.77	432.46	558.07
23	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	Railways	108.00	214.09	250.82
24	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR	NEFR	Railways	1000.00	1500.00	2408.10
25	KATIHAR - JOGBANI (GC)(NEFR)	NEFR	Railways	100.00	492.98	730.92

SN	PROJECT	AGENCY	SECTOR	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
26	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	NEFR	Railways	733.00	733.00	1275.88
27	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project	NEFR	Railways	1676.31	1676.31	3161.45
28	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR	NEFR	Railways	156.00	0.00	240.93
29	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	NEFR	Railways	170.00	170.00	392.26
30	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NEFR	Railways	727.56	727.53	911.23
31	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	NEFR	Railways	915.70	915.70	1343.13
32	KANPUR-KASGANJ-MATHURA(GC),NER	NER	Railways	395.00	1062.36	1354.57
33	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER)	NER	Railways	381.17	381.17	580.64
34	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	NER	Railways	323.40	323.40	495.55
35	ELECTRIFICATION OF MORADABAD-ROZA	RE	Railways	129.17	0.00	227.48
36	RENIGUNTA-GUNTAKAL(RE)	RVNL	Railways	168.34	0.00	354.18
37	RAJATGARH-BARANG(LD),ECOR	RVNL	Railways	166.16	0.00	248.79
38	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL)	RVNL	Railways	240.00	0.00	401.42
39	BILASPUR-URKURA (DL)	RVNL	Railways	151.52	0.00	321.48
40	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	Railways	133.41	207.00	212.13
41	RAICHUR-GUNTAKAL(DL)(SCR)	RVNL	Railways	136.62	0.00	231.38
42	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	SCR	Railways	124.43	495.68	584.06
43	NANDYAL-YERRAGUNTLA(NL),SCR	SCR	Railways	155.74	429.49	626.80
44	GADWAL - RAICHUR (NL), SCR	SCR	Railways	92.63	228.09	260.85
45	RANCHI-LOHARDAGA(GC),SER	SER	Railways	194.07	194.07	293.29
46	CALICUT-MANGALORE (DL) (SR)	SR	Railways	240.00	0.00	600.41
47	KARUR-SALEM(NL),SR	SR	Railways	155.55	229.88	736.89
48	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	Railways	100.00	100.00	504.71
49	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	SR	Railways	343.17	343.17	542.57
50	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR	SWR	Railways	295.00	412.91	509.89
51	KOTTUR-HARIHAR(NL),(SWR)	SWR	Railways	65.94	302.23	336.49

SN	PROJECT	AGENCY	SECTOR	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
52	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	NHAI	Road Transport & Highways	157.47	0.00	201.65
53	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2)	NHAI	Road Transport & Highways	367.49	0.00	453.68
54	GARH Mukteshwar-Muradabad (NHAI) OTHERS KM.93-149.25, NH-24	NHAI	Road Transport & Highways	275.00	0.00	306.19
55	Gurgaon-Kotputli Km 42.70 to 54.4 Km	NHAI	Road Transport & Highways	1673.70	0.00	2723.00
56	Chennai-Tada(Six lane)	NHAI	Road Transport & Highways	353.37	0.00	355.53
57	Kishangarh-Ajmer-Beawer	NHAI	Road Transport & Highways	795.00	0.00	1023.40
58	Pune-sholapur, pkg1	NHAI	Road Transport & Highways	1110.00	0.00	1802.10
59	MP/Maharashtra Border-Dhula	NHAI	Road Transport & Highways	835.00	0.00	1068.70
60	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	NHAI	Road Transport & Highways	940.00	0.00	1141.10
61	DELHI/ HARYANA BORDER TO ROHTAK	NHAI	Road Transport & Highways	486.00	0.00	587.32
62	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER	NHAI	Road Transport & Highways	464.00	0.00	535.25
63	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	NHAI	Road Transport & Highways	232.45	0.00	274.33
64	JAIPUR-REENGUS	NHAI	Road Transport & Highways	267.81	0.00	521.08
65	ROHTAK-BAWAL	NHAI	Road Transport & Highways	650.00	0.00	734.10
66	4 LANNING OF AHMEDABAD TO GODHARA	NHAI	Road Transport & Highways	1008.50	0.00	1097.80
67	INDORE-DEWAS(NH-3)	NHAI	Road Transport & Highways	325.00	0.00	376.84

SN	PROJECT	AGENCY	SECTOR	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
68	PANIPAT-ROHTAK	NHAI	Road Transport & Highways	807.00	0.00	884.84
69	AMRITSAR-PATHANKOT	NHAI	Road Transport & Highways	705.00	0.00	1158.30
70	KUNDUPUR-SURATHKAL & MANGLORE	NHAI	Road Transport & Highways	671.00	0.00	737.54
71	Armur to kadloor yellareddy	NHAI	Road Transport & Highways	390.56	0.00	631.65
72	Hyderabad-yadgiri N.H no-202	NHAI	Road Transport & Highways	388.00	0.00	506.40
73	Hazaribagh-Ranchi	NHAI	Road Transport & Highways	625.07	0.00	857.54
74	Hungund-Surathkal and Mangalore-Knt/Kerala Border	NHAI	Road Transport & Highways	946.00	0.00	1394.40
75	Jaipur-Tonk-Deoli	NHAI	Road Transport & Highways	792.06	0.00	1387.70
76	Hyderabad-Vijaywada Km. 40 to 221.50 Km	NHAI	Road Transport & Highways	1740.00	0.00	1848.50
77	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km)	NHAI	Road Transport & Highways	1108.00	0.00	3460.60
78	Chilikaluripet-Vijaywada 6 lane (km 355 to Km 434.15)	NHAI	Road Transport & Highways	572.30	0.00	691.40
79	Surat- Dahisar(Six Lane) Km 263 to Km 502	NHAI	Road Transport & Highways	1693.75	0.00	2659.00
80	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	NHAI	Road Transport & Highways	557.00	0.00	930.92
81	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68	NHAI	Road Transport & Highways	941.00	0.00	1901.00
82	TRICHY - KORUR NH-67	NHAI	Road Transport & Highways	516.00	0.00	760.07
83	JHANSI TO LALITPUR, NH-25,26	NHAI	Road Transport & Highways	355.06	0.00	469.55

SN	PROJECT	AGENCY	SECTOR	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
84	GWALIOR BYPASS, NH-75,3	NHAI	Road Transport & Highways	300.93	0.00	302.72
85	GANJAM-ICCHAPURUM,NH-5(NHAI)	NHAI	Road Transport & Highways	263.27	0.00	269.79
86	THANJAUR-TRICHY,NH-67(NHAI)	NHAI	Road Transport & Highways	280.00	0.00	581.49
87	NAGPUR-KONDHALI,NH-6(NHAI)	NHAI	Road Transport & Highways	168.00	0.00	457.30
88	HAPUR-GARH Mukteswar (Others) KM.58-93, NH-24	NHAI	Road Transport & Highways	220.00	0.00	277.83
89	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402	NHAI	Road Transport & Highways	240.00	0.00	294.12
90	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0	NHAI	Road Transport & Highways	340.68	0.00	385.28
91	AURANG-RAIPUR, NH-6, KM.232 TO KM.281	NHAI	Road Transport & Highways	190.00	0.00	259.75
92	DAKOBA TO NAGAON (NH-36)(NHAI)	NHAI	Road Transport & Highways	225.00	0.00	281.21
93	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	NHAI	Road Transport & Highways	195.00	0.00	205.46
94	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	NHAI	Road Transport & Highways	237.80	0.00	248.21
95	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	NHAI	Road Transport & Highways	332.94	0.00	389.13
96	DHARAMTUL TO SONAPUR (AS-19)	NHAI	Road Transport & Highways	200.00	0.00	231.15
97	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	NHAI	Road Transport & Highways	160.00	0.00	175.99
98	NALBARI T BIJNI (AS-7)	NHAI	Road Transport & Highways	208.00	0.00	266.19
99	NALBARI TO BIJNI (AS-6)	NHAI	Road Transport & Highways	225.00	0.00	240.75

SN	PROJECT	AGENCY	SECTOR	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
100	GUWAHATI TO NALBARI (AS-5)	NHAI	Road Transport & Highways	198.16	0.00	210.81
101	ASSAM/WB BORDER TO GAIRKATTA (WB-1)	NHAI	Road Transport & Highways	221.82	0.00	284.81
102	SONAPUR TO GUWAHTI (AS-3)	NHAI	Road Transport & Highways	245.00	0.00	491.21
103	NAGAON TO DHARAMTUL (AS-2)	NHAI	Road Transport & Highways	264.72	0.00	287.76
104	NALBARI TO BIJNI (AS-8)	NHAI	Road Transport & Highways	200.00	0.00	274.19
105	JHAJHARPUR TO DARBANGA (BR-7)	NHAI	Road Transport & Highways	340.00	0.00	541.94
106	KOTA BYPASS,RJ-4, NH-76 (NHAI)	NHAI	Road Transport & Highways	275.00	0.00	279.36
107	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI)	NHAI	Road Transport & Highways	151.30	0.00	190.52
108	SAGAR - RAJMARG CHORAH, KM 211 TO KM 255, NH-26 (NHAI)	NHAI	Road Transport & Highways	203.43	0.00	237.75
109	RAJMARG CHORAH TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI)	NHAI	Road Transport & Highways	251.03	0.00	309.92
110	RAJMARG CHORAH TO LAKHNANDON, KM 351 TO KM 405.7, NH-26 (NHA)	NHAI	Road Transport & Highways	229.91	0.00	262.25
111	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	Shipping & Ports	245.67	298.17	326.08
112	67.5 MW TG-5 AUX. S' TEM EMERGENCY POWER REQUIREMENT EXP. UNIT	RINL	Steel	230.00	0.00	248.53

Ahead

S.No	Project	DOA	DOC Original	DOC Revised	DOC Anticipated	COST Original	Cost Anticipated
1	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT	1/2010	01/2013	12/2012	12/2012	1478.63	1478.63
2	Expansion of Rourkela Steel Plant	9/2008	11/2013	N.A.	03/2013	11812	11812
3	Udhna-Jalgaon with electrification(doubling) (WR)	4/2008	03/2014	N.A.	03/2013	1389.62	1389.62
4	Acquistion of three(3) nos of 6500TEU Cellular container vessels from M/S stx shipbuilding co. ltd.	10/2010	12/2013	N.A.	10/2013	1028.1	1028.1
5	Setting up of Single Point Mooring (SPM) and allied facilities off Veera in Gulf of Kutch on BOT bas	2/2011	05/2013	N.A.	03/2013	830	621.53

List of project Without Original Date of Commissioning

(Aug,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Steel</u>									
1	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,Karnataka	04/2011	572.00	572.00	165.84	-	04/2013	-	11/19
2	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,Karnataka	02/2011	898.55	898.55	106.43	-	05/2013	-	16/21
	Total		1,470.55	1,470.55	272.27				27/40
<u>Petroleum</u>									
3	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00	898.00	893.30	-	03/2012	5(R3)	0/53
4	EURO-IV DHDT - [N16000109]CPCL,Tamil Nadu	09/2008	2,615.69	2,615.69	1,941.28	-	09/2012	-	116/116
5	CDU/VDU-II - [N16000110]CPCL,Tamil Nadu	03/2010	333.99	333.99	177.15	-	09/2012	-	33/36
6	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE - [N16000070]GAIL,Multi State	07/2009	238.68	302.00	217.12	-	01/2012	9(R3)	1/1
7	PARADIP REFINERY PROJECT - [N16000058]IOCL,Orissa	02/2009	29,777.00	30,426.00	17,280.00	-	09/2013	0(R3)	167/100
	Total		33,721.36	34,575.68	20,508.85				317/306
<u>Power</u>									
8	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01	623.44	325.05	-	07/2013	0(R3)	6/29
9	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttaranchal	11/2006	2,978.48	2,978.48	1,528.00	-	09/2015	-	7/14
	Total		3,399.49	3,601.92	1,853.05				13/43
<u>Railways</u>									
10	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55	712.00	736.89	-	10/2012	-	0/0
11	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17	900.00	542.57	-	12/2012	-	0/0
12	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00	944.55	509.89	-	01/2013	-	0/0
13	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19	218.19	162.70	-	02/2013	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
14	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 1,010.00	2,200.00	182.53	- -	03/2013	-	0/0
15	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	194.48	- -	03/2013	-	0/0
16	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	162.87	92.71	- -	03/2013	-	0/0
17	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	1,029.00	753.56	- -	03/2013	-	0/0
18	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	1,100.00	254.10	- -	03/2013	-	0/0
19	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 915.70	1,717.29	1,343.13	- -	03/2013	-	0/0
20	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	810.78	113.80	- -	03/2013	-	0/0
21	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	194.91	- -	12/2013	-	0/0
22	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 323.40	750.89	495.55	- -	03/2014	-	0/1
23	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	230.03	145.43	- -	03/2014	-	0/0
24	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 200.00	385.20	112.60	- -	03/2014	-	0/0
25	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	703.17	242.01	- -	03/2015	-	0/0
26	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	359.86	1.22	- -	03/2015	-	0/0
27	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	324.66	180.42	- -	03/2015	-	0/0
	Total		5,654.70 -	13,544.50	6,258.50				0/1
Road Transport & Highways									
28	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI,Karnataka	09/2010	946.00 -	946.00	1,394.40	- -	03/2013	-	3/3
29	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,Karnataka	09/2010	671.00 -	671.00	737.54	- -	03/2013	-	2/3
30	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00 -	680.00	99.39	- -	04/2013	-	2/2
31	DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka	12/2010	453.00 -	453.00	351.33	- -	06/2013	-	1/1
32	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka	12/2010	480.00 -	480.00	417.00	- -	10/2013	-	2/2
33	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,Karnataka	03/2011	839.00 -	839.00	302.14	- -	12/2013	-	0/1

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
Total			4,069.00	4,069.00	3,301.80				10/12
Grand Total			48,315.10	57,261.65	32,194.47				367/402

List of project Without Date of Commissioning

Date of Commissioning					
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
<u>Atomic Energy</u>					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVINI,Tamil Nadu	09/2003	3,492.00 -	09/2010 -	01/2012
2	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29 -	04/2011 04/2011	04/2012
	Total		4,598.29 -		
<u>Civil Aviation</u>					
3	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	01/2011 02/2012	02/2012
	Total		1,808.00 -		
<u>Coal</u>					
4	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03 -	03/2012 -	-
	Total		249.03 -		
<u>Fertilisers</u>					
5	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00 -	07/2011 -	04/2012
6	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00 -	07/2011 -	07/2012
	Total		763.00 -		
<u>Petroleum</u>					
7	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra	05/2008	333.40 837.54	05/2010 04/2012	07/2012
8	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	- -	-
9	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	08/2009	246.81 -	04/2012 -	-
10	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 394.00	- 08/2011	-
	Total		2,388.21 -		
<u>Power</u>					
11	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45 1,007.16	12/2007 12/2009	-
12	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	09/2010 -	-
	Total		1,074.14 -		

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>Railways</u>				
13	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94 604.04	03/1998 08/2005	08/2005
14	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30	06/2007 -	06/2007
15	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	07/2008 -	07/2008
16	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	- 05/2009	05/2009
17	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd	04/1996	371.36 768.87	- 03/2010	03/2010
18	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 3,176.10	12/2006 08/2010	08/2010
19	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	12/2010
20	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 293.74	12/2010 12/2010	12/2010
21	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	02/2010 02/2011	02/2011
22	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 405.17	06/1999 03/2011	03/2011
23	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	- -	03/2011
24	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	05/2008 03/2011	03/2011
25	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	12/2009 03/2011	03/2011
26	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	- 03/2009	03/2011
27	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 -	03/2009 12/2009	03/2011
28	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	03/2011 03/2011	03/2011
29	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011
30	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100007]NCR,Multi State	04/1985	158.77 432.46	03/1994 -	12/2011
31	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 1,185.00	- 09/2009	12/2011
32	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	- -	02/2012
33	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	- 12/2009	02/2012
34	Dakshin-barasal-lakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	12/2011 02/2012	02/2012
35	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	- -	03/2012
36	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	02/2009 -	03/2012
37	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	- -	03/2012
38	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	- -	03/2012

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
39	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 381.17	- -	03/2012
40	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	- -	03/2012
41	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	- -	03/2012
42	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	03/2010 -	03/2012
43	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 -	- -	03/2012
44	MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N22000093]MRTP,Maharashtra	04/2003	3,125.20 4,174.40	06/2011 03/2012	03/2012
45	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	03/2012 -	03/2012
46	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	03/2011 -	03/2012
47	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhandd	04/2008	167.73 167.73	03/2012 -	03/2012
48	CHURCHGATE-VIRAR:CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	653.84 1,302.12	06/2013 06/2012	06/2012
49	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	07/2012 07/2012	07/2012
50	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	12/2012 -	-
51	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	03/1998 -	-
52	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	- -	-
53	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	04/2003 03/2010	-
54	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,047.00	- -	-
55	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91 418.17	- -	-
56	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23 -	02/2015 -	-
57	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-
58	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	- -	-
59	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	- 03/2010	-
60	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00 -	- -	-
61	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 2,957.21	07/2005 -	07/2005
62	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 100.00	- -	-
63	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 901.62	- -	-
64	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar	04/2001	104.79 -	- -	-

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
65	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	- -	-
66	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	- -	-
67	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'I-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	- -	-
68	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 227.40	- -	-
69	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 582.83	- -	-
70	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24 -	03/2012 -	03/2012
71	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	03/2011 -	03/2011
	Total		19,546.41 -		
Shipping & Ports					
72	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 1,571.60	10/2008 -	10/2008
73	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84 -	- 01/2009	01/2009
74	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	04/2009 11/2009	02/2011
75	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	03/2012 -	03/2012
76	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	10/2008 -	-
	Total		3,904.91 -		
Telecommunications					
77	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84 -	10/2009 -	03/2011
78	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38 -	10/2007 -	-
79	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00 -	03/2009 -	-
80	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	03/2010 -	-
81	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	02/2007 12/2010	-
82	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	03/2010 -	-
	Total		2,997.75 -		
Urban Development					
83	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	04/2009 -	-
	Total		114.18 -		

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
Grand Total			37,443.92		

List of On schedule Projects

(Aug,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Civil Aviation</u>						
1	GAGAN PROJECT - [N04000065	9/2008	626.00 -	626.00	372.05	06/2013 -	06/2013
2	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II [N04000070	2/2011 -	452.00 -	452.00	1.20	02/2015 -	02/2015
	Total		1,078.00 -	1,078.00	373.25		
	<u>Coal</u>						
3	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019	11/2006	168.97 -	168.97	40.35	03/2014 03/2014	03/2014
4	JALLARAM SHAFT PROJECT - [N06000025	9/2007	467.78 -	467.78	12.31	03/2013 -	03/2013
5	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034	12/2007	490.00 -	490.10	115.68	03/2017 -	03/2017
6	KANIHA OCP, MCL, (10.0 Mty) - [N06000035	12/2007	457.77 -	457.77	110.47	03/2013 -	03/2013
7	GOPAL PRASAD OCP - [N06000042	2/2008	395.87 -	395.87	71.12	03/2015 -	03/2015
8	TALABIRA OCP - [N06000043	3/2008	447.72 -	447.72	44.49	03/2016 -	03/2016
9	PELMA OCP(10.00MTY) - [N06000045	7/2008	448.32 -	448.32	-	03/2015 -	03/2015
10	Batura OCP (2.0 MTY) - [N06000049	9/2008	203.82 -	203.82	-	03/2015 -	03/2015
11	RAJMAHAL OC EXP. - [N06000056	9/2009	153.82 -	153.82	25.44	03/2014 -	03/2014
12	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068	11/2008	479.63 -	479.63	109.71	03/2013 -	03/2013
13	RKP OCP PHASE-I - [N06000079	3/2010	209.78 -	209.78	26.63	03/2015 -	03/2015
14	Purnadih OCP - [N06000085	7/2008	210.98 -	210.98	87.89	03/2013 -	03/2013
15	Rajrappa RCE OCP - [N06000087	12/2009	510.85 -	510.85	268.59	03/2016 -	03/2016
16	KARMA OCP - [N06000088	6/2009	162.46 -	162.46	30.89	03/2014 -	03/2014
17	Kistaram OCP - [N06000089	11/2010	242.29 -	242.29	-	03/2015 -	03/2015
18	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093	7/2011	162.76 -	162.76	2.48	03/2015 -	03/2015
19	JALAGAM VENGALA RAO OCP - [N06000094	7/2011	447.06 -	447.06	-	03/2015 -	03/2015
20	MANIKPUR OC EXPANSION - [N06000081	11/2009	321.42 -	321.50	203.67	03/2014 -	03/2014

(Aug,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
21	DIPKA EXPANSION OCP (SECL) (20 MTY) - [060100094	12/2009	1,943.66 -	1,943.66	1,211.06	03/2014 -	03/2014
22	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091	6/2011	1,131.28 -	1,131.28	1.51	03/2018 03/2018	03/2018
23	KUSMUNDA EXPN.OCP(SECL)(10MTY) - [N06000008	6/2008	1,188.31 -	1,188.31	668.76	03/2013 -	03/2013
24	GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093	6/2010	2,675.67 -	2,675.67	1,383.91	03/2014 -	03/2014
25	Muraidih UG Turn-key Project - [N06000096	2/2011	339.88 -	339.88	-	04/2014 -	04/2014
26	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099	4/2012	258.56 -	258.56	39.30	03/2016 -	03/2016
27	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082	11/2009	150.59 -	198.59	84.63	03/2016 -	03/2016
28	Moonidih XV Seam UG - [N06000098	8/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015
	Total		14,899.52 -	14,947.70	4,538.89		
<u>Fertilisers</u>							
29	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGEVER PROJECT - [N08000005	1/2010	1,294.19 -	1,294.19	639.95	01/2013 -	01/2013
30	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGEVER PROJECT - [N08000004	1/2010	1,292.84 -	1,292.84	671.00	01/2013 -	01/2013
	Total		2,587.03 -	2,587.03	1,310.95		
<u>Petrochemicals</u>							
31	Assam gas Cracker project - [N16000106	4/2006	5,460.61 -	8,920.00	5,197.24	12/2013 12/2013	12/2013
	Total		5,460.61 -	8,920.00	5,197.24		
<u>Petroleum</u>							
32	IOR of B-173A Field - [N16000140	1/2012	352.49 -	352.49	-	03/2014 -	03/2014
33	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088	8/2009	1,793.00 -	1,793.00	676.77	09/2012 -	09/2012
34	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA [N16000112	8/2010	8,140.00 -	8,140.00	1,588.37	02/2014 -	02/2014
35	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY - [N16000081	4/2008	825.00 -	1,827.00	611.55	04/2013 04/2013	04/2013
36	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128	3/2011	861.79 -	756.65	11.81	05/2013 -	05/2013

(Aug,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
37	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127	6/2010	202.94 -	202.94	0.20	01/2014 -	01/2014
38	Ankleswar Redevelopment - [N16000122	11/2010	2,189.63 -	2,189.63	-	12/2014 -	12/2014
39	Integrated Development of B-127 fields - [N16000131	12/2011	2,059.63 -	2,059.63	-	03/2015 -	03/2015
40	Wax Project - [N16000101	6/2010	576.60 -	576.60	60.70	12/2013 12/2013	12/2013
41	Construction of tanks and blending facility at Vadinar - [N16000115	2/2009	267.00 -	267.00	208.23	09/2012 09/2012	09/2012
42	BUTENE-1 PROJECT AT PANIPAT - [N16000139	2/2012	190.00 -	190.00	4.54	03/2014 -	03/2014
43	Fire water network at Uran - [N16000141	5/2010	171.68 -	171.68	-	06/2013 -	06/2013
44	Heera and South Heera Redevelopment Ph-II - [N16000132	3/2012	5,608.40 -	5,608.40	-	05/2015 -	05/2015
45	Mehesana Redevelopment - [N16000121	11/2010	3,823.00 -	3,823.00	701.81	04/2015 -	04/2015
46	Pipeline Replacement Project-3 - [N16000137	4/2012	2,547.26 -	1,417.00	-	05/2014 -	05/2014
47	Butadiene Extraction Unit(BDEU) at Panipat - [N16000108	11/2009	341.50 -	341.50	110.19	02/2013 -	02/2013
48	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY [N16000069	3/2009	3,284.00 -	2,174.00	1,092.04	09/2012 09/2012	09/2012
49	Development of Western Periphery of MH South Field - [N16000136	4/2012	600.17 -	600.17	-	12/2014 -	12/2014
50	Ahmedabad Redevelopment - [N16000120	11/2010	1,916.10 -	1,916.10	614.17	12/2014 -	12/2014
51	Development of C-26 Cluster Fields - [N16000133	3/2012	2,592.17 -	2,592.17	-	05/2014 -	05/2014
52	Development of WO-16 Cluster Fields - [N16000105	6/2010	2,523.00 -	2,523.00	176.69	01/2014 -	01/2014
	Total		40,865.36 -	39,521.96	5,857.07		
<u>Power</u>							
53	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126	3/2012	206.44 -	206.44	22.20	06/2014 -	06/2014
54	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125	3/2012	9,569.76 -	9,569.76	27.70	06/2015 -	06/2015
55	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA MEGA POWER PROJECT - [N18000046	12/2008	7,031.88 -	7,031.88	3,810.70	12/2012 -	12/2012
56	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109	10/2011	487.49 -	487.49	60.40	06/2014 -	06/2014
57	Northern region system strenghening scheme XVI - [N18000094	7/2010	752.64 -	752.64	196.30	07/2013 -	07/2013

(Aug,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
58	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]	12/2011	2,422.66 -	2,422.66	73.00	08/2014 -	08/2014
59	MOUDA STPP STAGE 2 - [N18000132]	3/2012	7,921.47 -	7,921.47	536.00	09/2016 -	09/2016
60	SOLAPUR STPP - [N18000133]	3/2012	9,395.18 -	9,395.18	666.00	11/2016 -	11/2016
61	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]	8/2011	425.51 -	425.51	90.10	10/2013 -	10/2013
62	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	297.33	22.20	08/2014 -	08/2014
63	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]	9/2011	1,366.34 -	1,366.34	204.80	12/2013 -	12/2013
64	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1 - [N18000121]	2/2012	324.33 -	324.33	1.90	08/2014 -	08/2014
65	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118]	1/2012	259.28 -	259.28	14.60	01/2014 -	01/2014
66	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]	11/2011	723.63 -	723.63	43.20	11/2014 -	11/2014
67	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNAM OF ANDHRA PRADESH(PGCIL) - [N18000111]	8/2011	1,637.34 -	1,637.34	239.60	08/2014 -	08/2014
68	Establishment of pooling stations at Rajgarh and raipur for IPP generation projects in chattisgarh - [N18000092]	12/2010	1,719.52 -	1,719.52	582.60	08/2013 -	08/2013
69	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]	1/2012	1,422.85 -	1,422.85	104.70	01/2015 -	01/2015
70	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]	10/2011	558.26 -	558.26	63.80	11/2013 -	11/2013
71	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]	5/2011	1,961.87 -	1,961.87	368.10	05/2014 -	05/2014
72	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]	12/2011	1,746.65 -	1,746.65	47.90	08/2014 -	08/2014
73	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]	12/2011	552.44 -	552.44	47.40	02/2014 -	02/2014
74	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]	12/2011	901.77 -	901.77	59.60	08/2014 -	08/2014
75	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]	3/2012	213.78 -	213.78	-	03/2014 -	03/2014
76	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPs GENERATION PROJECTS IN CHATTISGARH - [N18000112]	11/2011	2,127.51 -	2,127.51	230.30	07/2014 -	07/2014

(Aug,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
77	Transmission system for phase-I generation projects in orissa-part B - [N18000093]	12/2010	2,743.19 -	2,743.19	775.80	12/2013 -	12/2013
78	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]	9/2010	2,074.86 -	2,074.86	647.30	03/2013 -	03/2013
79	NORTHERN REGION SYSTEM STRENGHTENING SCHEME-XX [N18000088]	10/2010	182.68 -	182.68	47.10	01/2013 -	01/2013
80	KUDGI STPP STAGE 1 - [N18000131]	12/2011	15,166.19 -	15,166.19	959.00	12/2016 -	12/2016
81	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000107]	8/2011	1,391.97 -	1,391.97	343.00	12/2013 -	12/2013
82	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUB STATION AT KALA IN UT DNH - [N18000102]	7/2011	181.93 -	181.93	48.40	07/2013 -	07/2013
83	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]	2/2012	1,927.16 -	1,927.16	33.90	10/2014 -	10/2014
84	Transmission system for transfer of power from Gen.proj in sikkim to NR/WR part-B [N18000099]	3/2011	1,585.12 -	1,585.12	366.80	11/2013 -	11/2013
85	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B [N18000129]	2/2012	3,201.44 -	3,201.44	45.80	10/2014 -	10/2014
86	Common System Associated with Coastal Energen Private Limited and Ind-Barath Power(Madras) Limited L - [N18000103]	9/2011	1,940.13 -	1,940.13	243.10	09/2014 -	09/2014
87	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]	2/2012	1,310.85 -	1,310.85	102.50	02/2015 -	02/2015
88	Transmission system for phase-I gen.proj.in orissa part-C - [N18000096]	3/2011	2,569.25 -	2,569.25	582.60	03/2014 -	03/2014
89	Transm System for development of Pooling stn. in NR part of West Bengal & Transfer of power from BHU - [N18000077]	4/2010	4,404.57 -	4,404.57	334.70	01/2015 -	01/2015
90	Northern Region system strengthening scheme-XXII - [N18000091]	12/2010	209.78 -	209.78	70.90	08/2013 -	08/2013
91	Transmission system associated with krishnapatnam- Part-A - [N18000090]	12/2010	779.21 -	779.21	525.10	08/2013 -	08/2013
92	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]	3/2012	198.63 -	198.63	-	09/2014 -	09/2014
93	Supplementary transmission associated with vellur TPS - [N18000097]	8/2010	170.36 -	170.36	45.60	04/2013 -	04/2013
94	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID [N18000130]	6/2012	1,263.26 -	1,263.26	20.60	11/2014 -	11/2014
	Total		95,326.51 -	95,326.51	12,705.30		
Railways							

(Aug,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
95	AGARTALA SABROOM, NL, NEFR - [N22000099]	4/2008	813.34 -	1,141.75	407.49	03/2014 -	03/2014
96	SEVOK RANGPO, NEFR - [N22000102]	4/2008	1,339.48 -	3,380.58	52.63	12/2015 -	12/2015
97	New Work for Construction of Metro railway from Noapara-Barasai VIA Bimanbender (MTP) [N22000108]	4/2010	2,397.72 -	228.82	32.97	03/2016 -	03/2016
98	New Work for Construction of Metro railway from NSCB Airport to New Garia VIA Rajarhat (MTP) [N22000110]	4/2010	3,951.98 -	3,951.98	21.71	03/2016 -	03/2016
99	New Work for Construction of Metro railway from Joka to Binoy Badal Dinesh Bagh. [N22000111]	4/2010	2,619.02 -	2,913.51	151.51	03/2016 -	03/2016
100	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]	4/2008	829.74 -	829.74	6.07	03/2015 -	03/2015
101	Jaipur - Ringus - Churu and Sikar - Loharu Guage Conversion (NWR) [N22000113]	4/2008	653.19 -	653.46	175.60	03/2014 -	03/2014
102	Suratpura - Hanumangarh - Sriganganagar Guage Conversion (NWR) [N22000114]	4/2008	516.23 -	516.23	238.77	03/2014 -	03/2014
103	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]	4/2008	394.14 -	404.39	0.49	03/2013 -	03/2013
104	New Line from Dimapur to Zubza(Kohima) national project (NEFR) - [N22000124]	4/2006	850.00 -	850.00	8.44	03/2015 -	03/2015
	Total		14,364.84 -	14,870.46	1,095.68		
Road Transport & Highways							
105	PUNE-SHOLAPUR,Pkg-II - [N24000193]	9/2011	835.00 -	835.00	104.67	01/2014 -	01/2014
106	Two laning of Trichy - Karaikudi and Trychi Bypass - [N24000176]	5/2010	374.00 -	374.00	75.23	05/2013 -	05/2013
107	DEOLI-KOTA - [N24000148]	1/2011	953.00 -	593.00	371.11	07/2013 -	07/2013
108	ROHTAK-BAWAL - [N24000169]	5/2011	650.00 -	650.00	734.10	11/2013 -	11/2013
109	JAIPUR-REENGUS - [N24000198]	8/2010	267.81 -	267.81	521.08	02/2013 -	02/2013
110	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 [N24000171]	6/2011	535.00 -	535.00	-	12/2013 -	12/2013
111	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]	5/2011	511.54 -	511.54	238.72	11/2013 -	11/2013
112	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]	9/2011	2,848.00 -	2,848.00	677.05	03/2014 -	03/2014
113	PANIKHOLI-RIMOLI - [N24000197]	3/2012	1,410.00 -	1,410.00	148.10	09/2014 -	09/2014
114	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]	3/2010	1,509.10 -	1,509.10	1,427.90	09/2012 -	09/2012
115	2 laning of Dindigul - Perigulam Theni- kumili - [N24000177]	9/2011	485.00 -	485.00	72.63	08/2013 -	08/2013

(Aug,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
116	Indore-Jhabua-Gujrat/MP - [N24000136	10/2010	1,175.00 -	1,175.00	138.67	04/2013 -	04/2013
117	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134	4/2010	1,740.00 -	1,740.00	1,848.50	10/2012 -	10/2012
118	Talegaon-amravati - [N24000140	11/2009	567.00 -	567.00	471.21	11/2013 -	11/2013
119	2-LANNING OF SHILONG BYPASS - [N24000181	2/2011	226.00 -	226.00	220.00	02/2014 -	02/2014
120	4-laning of Brahampore-Faraka - [N24000203	2/2011	998.79 -	998.79	530.25	08/2013 -	08/2013
121	2 Laning of Muzaffarpur - Sonbarsa - [N24000174	5/2011	511.54 -	511.54	238.72	11/2013 -	11/2013
122	PANIPAT-ROHTAK - [N24000151	4/2011	807.00 -	807.00	884.84	10/2014 -	10/2014
123	4-laning of Barhi-Hazaribagh - [N24000191	2/2012	398.00 -	398.00	261.02	02/2014 -	02/2014
124	Hazaribagh-Ranchi - [N24000141	8/2010	625.07 -	625.07	857.54	01/2013 -	01/2013
125	NIROLI-ROXY-RAJAMUNDA - [N24000194	7/2011	586.00 -	586.00	237.55	01/2014 -	01/2014
126	Kandla - Mundra port - [N24000175	1/2011	953.88 -	953.88	386.37	07/2013 -	07/2013
127	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205	12/2011	1,047.00 -	1,047.00	148.11	06/2014 -	06/2014
128	MUZAFFARNAGAR-HARIDWAR - [N24000201	9/2011	754.00 -	754.00	384.91	03/2013 -	03/2013
129	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186	10/2011	375.09 -	375.09	40.11	04/2014 -	04/2014
130	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167	12/2010	1,008.50 -	1,008.50	1,097.80	06/2013 -	06/2013
131	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER [N24000196	11/2011	909.00 -	909.00	844.05	05/2014 -	05/2014
132	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208	7/2012	291.36 -	291.36	9.66	01/2014 -	01/2014
133	NAGPUR-WAINGANGA BRIDGE - [N24000210	4/2012	484.19 -	484.19	-	10/2014 -	10/2014
134	MURADABAD-BAREILY - [N24000154	4/2010	1,267.00 -	1,267.00	1,264.30	06/2013 -	06/2013
135	2laning with PS Gopalganj-Chappra - [N24000190	12/2011	325.00 -	325.00	130.53	05/2014 -	05/2014
136	BHUBANESWAR TO PURI - [N24000195	3/2011	500.29 -	500.29	380.32	08/2013 -	08/2013
137	GHAZIABAD-ALIGARH NH-91 - [N24000170	2/2011	1,141.00 -	1,141.00	679.81	08/2013 -	08/2013
138	PUNE-SATARA(NH-4) - [N24000156	10/2010	1,724.55 -	1,724.55	975.44	03/2013 -	03/2013
139	Jaipur-Tonk-Deoli - [N24000135	6/2010	792.06 -	792.06	1,387.70	12/2012 -	12/2012
140	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183	11/2011	1,535.00 -	1,535.00	822.95	05/2014 -	05/2014

(Aug,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
141	KRISHNANAGAR-BERHAMPUR - [N24000209	2/2012	702.16 -	702.16	150.41	07/2014 -	07/2014
142	4-laning of Faraka-Raiganj - [N24000202	2/2011	1,078.84 -	1,078.84	646.48	08/2013 -	08/2013
143	New 4 Lane elevated road from chennai airport- maduravoyal NH no.4 [N24000139	9/2010	1,655.00 -	1,655.00	426.98	09/2013 -	09/2013
144	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185	9/2011	574.00 -	574.00	403.96	03/2014 -	03/2014
145	4 LANNING OF GODHARA TO GUJARAT/MP BORDER [N24000168	3/2011	785.50 -	785.50	529.08	08/2013 -	08/2013
146	SAMAIKHIALI - GANDHIDHAM - [N24000179	9/2010	805.39 -	805.39	308.07	03/2013 -	03/2013
147	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750- 356.502 KM [N24000145	11/2010	1,585.00 -	1,585.00	957.76	05/2013 -	05/2013
148	Tirupati - Tiruthani - Chennai - [N24000178	4/2011	571.00 -	571.00	-	10/2013 -	10/2013
149	4 LANING OF NAGPUR-BETUL - [N24000155	2/2011	2,498.76 -	2,498.76	804.19	08/2014 -	08/2014
150	PATNA-MUZZAFFARPUR - [N24000165	8/2010	671.30 -	671.30	586.44	02/2013 -	02/2013
151	BAREILY-SITAPUR - [N24000200	3/2011	1,046.00 -	1,046.00	138.55	09/2013 -	09/2013
152	CHENGAPALLI TO COIMBATORE BYPASS KM- 102.035-144.740 KM [N24000144	9/2010	852.00 -	852.00	667.28	03/2013 -	03/2013
153	SRINAGAR TO BANIHAL - [N24000189	6/2011	1,100.70 -	1,100.70	-	06/2014 -	06/2014
154	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150	2/2011	193.45 -	193.45	31.47	11/2012 -	11/2012
155	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY [N24000173	6/2011	600.00 -	600.00	75.85	06/2013 -	06/2013
156	4-laning of Raiganj-Dalkola - [N24000204	2/2011	580.43 -	580.43	218.49	08/2013 -	08/2013
157	4-LANNING OF CHAPRA-HAJIPUR - [N24000187	1/2011	575.00 -	575.00	425.81	07/2013 -	07/2013
158	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172	9/2011	1,250.00 -	1,250.00	12.48	12/2013 -	12/2013
159	BEAWAR-PALI-PINDWARA - [N24000199	12/2011	2,388.00 -	2,388.00	371.76	06/2014 -	06/2014
160	JORBAT - BARAPANI - [N24000180	1/2011	536.00 -	536.00	387.88	01/2014 -	01/2014
	Total		51,169.30 -	50,809.30	25,753.89		
Shipping & Ports							

(Aug,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
161	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CARRIERS - [N25000031	8/2008	1,066.91 -	968.35	777.97	09/2012 -	09/2012
162	Acquisition of two(2) Nos. of 317000 DWT very large crude carriers from M/S Jiangsu rongsheng heavy - [N25000053	10/2010	966.46 -	994.82	248.23	02/2014 -	02/2014
	Total		2,033.37 -	1,963.17	1,026.20		
<u>Steel</u>							
163	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Oddisha - [N12000079	1/2012	254.90 -	254.90	-	12/2014 -	12/2014
164	INSTALLATION OF 1x45 MVA Submerged Arc Furnace AT CHANDRAPUR FERRO PLANT(CFP) - [N12000076	12/2011	187.33 -	187.33	-	12/2013 -	12/2013
165	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, chattisgarh - [N12000078	7/2012	332.65 -	332.65	-	08/2014 -	08/2014
	Total		774.88 -	774.88	.00		
<u>Urban Development</u>							
166	FARIDABAD EXTENSION - [N28000057	9/2011	2,494.00 -	2,494.00	69.58	09/2014 -	09/2014
167	DELHI MRTS PHASE-III - [N28000056	9/2011	35,242.00 -	35,242.00	709.91	03/2016 -	03/2016
	Total		37,736.00 -	37,736.00	779.49		
	Grand Total		266,295.42	268,535.01	58,637.96		

List of Projects Without Milestones

(Aug,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
<u>Atomic Energy</u>						
1	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29 -	04/2011 04/2011	04/2012	0/0
	Total		1,106.29 -			0/0
<u>Civil Aviation</u>						
2	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	01/2011 02/2012	02/2012	0/0
3	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	05/2011 03/2012	10/2012	0/0
4	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61 -	05/2012 -	12/2012	0/0
5	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	01/2011 04/2013	04/2013	0/0
6	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00 -	06/2013 -	06/2013	0/0
7	DEVLOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT - [N04000070]AAI,Punjab	02/2011	452.00 -	02/2015 -	02/2015	0/0
	Total		5,473.58 -			0/0
<u>Coal</u>						
8	KARMA OCP - [N06000088]CCL,Jharkhandd	06/2009	162.46 -	03/2014 -	03/2014	0/0
9	Muraidih UG - [N06000096]BCCL,Jharkhandd	02/2011	339.88 -	04/2014 -	04/2014	0/0
10	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04 535.10	03/2012 03/2015	03/2015	0/0
11	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhandd	08/2011	1,230.27 -	04/2015 -	04/2015	0/0
12	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,Chhatisgarh	04/2012	258.56 -	03/2016 -	03/2016	0/0
13	KHADIA EXPANSION OPENCAST PROJECT 4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28 1,131.28	03/2018 03/2018	03/2018	0/0
	Total		3,868.49 -			0/0
<u>Fertilisers</u>						
14	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00 -	07/2011 -	04/2012	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
15	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00 -	07/2011 -	07/2012	0/0
	Total		763.00 -			0/0
<u>Steel</u>						
16	INSTALLATION OF 1x45 MVA Submerged Arc Furnace AT - [N12000076]SAIL,Maharashtra	12/2011	187.33 -	12/2013 -	12/2013	0/0
17	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, chattisga - [N12000078]SAIL,Delhi	07/2012	332.65 -	08/2014 -	08/2014	0/0
18	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Oddisha - [N12000079]SAIL,Delhi	01/2012	254.90 -	12/2014 -	12/2014	0/0
	Total		774.88 -			0/0
<u>Petroleum</u>						
19	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra	05/2008	333.40 837.54	05/2010 04/2012	07/2012	0/0
20	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	09/2011 03/2012	09/2012	0/0
21	Construction of tanks and blending facility at Vad - [N16000115]IOCL,Gujarat	02/2009	267.00 -	09/2012 09/2012	09/2012	0/0
22	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	05/2010 05/2012	10/2012	0/0
23	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11 -	04/2011 -	10/2012	0/0
24	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 12,160.26	01/2012 -	11/2012	0/0
25	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	12/2011 -	01/2013	0/0
26	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	05/2010 03/2013	03/2013	0/0
27	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	03/2011 05/2011	03/2013	0/0
28	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	08/2012 -	03/2013	0/0
29	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	12/2008 04/2013	04/2013	0/0
30	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	09/2010 03/2012	04/2013	0/0
31	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	07/2012 -	04/2013	0/0
32	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	03/2013 -	04/2013	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
33	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	03/2010 03/2012	05/2013	0/0
34	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	07/2010 05/2012	05/2013	0/0
35	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79 -	05/2013 -	05/2013	0/0
36	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	04/2006 06/2012	06/2013	0/0
37	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 -	06/2012 -	06/2013	0/0
38	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	09/2012 -	06/2013	0/0
39	Fire water network at Uran - [N16000141]ONGC,Maharashtra	05/2010	171.68 -	06/2013 -	06/2013	0/0
40	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	09/2011 -	08/2013	0/0
41	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	09/2012 -	09/2013	0/0
42	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	11/2012 -	10/2013	0/0
43	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	06/2012 -	10/2013	0/0
44	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	03/2013 -	11/2013	0/0
45	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	08/2010 03/2012	12/2013	0/0
46	Wax Project - [N16000101]NRL,Assam	06/2010	576.60 -	12/2013 12/2013	12/2013	0/0
47	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	01/2014 -	01/2014	0/0
48	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	08/2013 -	01/2014	0/0
49	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER - [N16000127]ONGC,Assam	06/2010	202.94 -	01/2014 -	01/2014	0/0
50	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00 -	02/2014 -	02/2014	0/0
51	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	03/2013 -	03/2014	0/0
52	Butene-1 at Panipat - [N16000139]IOCL,Haryana	02/2012	190.00 -	03/2014 -	03/2014	0/0
53	IOR of B-173A Field - [N16000140]ONGC,Multi State	01/2012	352.49 -	03/2014 -	03/2014	0/0
54	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 -	03/2013 -	04/2014	0/0
55	Development of C-26 Cluster Fields - [N16000133]ONGC,Maharashtra	03/2012	2,592.17 -	05/2014 -	05/2014	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
56	Pipeline Replacement Project-3 - [N16000137]ONGC,Multi State	04/2012	2,547.26 -	05/2014 -	05/2014	0/0
57	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	10/2010 -	12/2014	0/0
58	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10 -	12/2014 -	12/2014	0/0
59	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63 -	12/2014 -	12/2014	0/0
60	Development of Western Periphery of MH South Field - [N16000136]ONGC,Multi State	04/2012	600.17 -	12/2014 -	12/2014	0/0
61	Integrated Development of B-127 fields - [N16000131]ONGC,Maharashtra	12/2011	2,059.63 -	03/2015 -	03/2015	0/0
62	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00 -	04/2015 -	04/2015	0/0
63	Heera and South Heera Redevelopment Ph-II - [N16000132]ONGC,Maharashtra	03/2012	5,608.40 -	05/2015 -	05/2015	0/0
64	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	01/2013 -	07/2015	0/0
65	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	- -	-	0/0
66	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	08/2009	246.81 -	04/2012 -	-	0/0
	Total		104,446.52 -			0/0
Power						
67	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61 -	04/2012 -	10/2012	0/0
68	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.56 -	10/2010 01/2013	06/2013	0/0
69	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93 -	07/2013 -	07/2013	0/0
70	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	09/2009 06/2013	08/2013	0/0
71	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pr.	01/2007	2,047.03 -	01/2012 -	09/2013	0/0
72	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BA - [N18000124]PGCIL,Madhya pradesh	03/2012	213.78 -	03/2014 -	03/2014	0/0
73	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARK - [N18000113]PGCIL,Multi State	12/2011	2,422.66 -	08/2014 -	08/2014	0/0
74	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123]PGCIL,Multi State	03/2012	198.63 -	09/2014 -	09/2014	0/0
75	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,Multi State	11/2011	723.63 -	11/2014 -	11/2014	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
76	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,Multi State	06/2012	1,263.26 -	11/2014 -	11/2014	0/0
77	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP P - [N18000120]PGCIL,Maharashtra	02/2012	1,310.85 -	02/2015 -	02/2015	0/0
78	MOUDA STPP STAGE 2 - [N18000132]NTPC,Maharashtra	03/2012	7,921.47 -	09/2016 -	09/2016	0/0
79	SOLAPUR STPP - [N18000133]NTPC,Maharashtra	03/2012	9,395.18 -	11/2016 -	11/2016	0/0
80	KUDGI STPP STAGE 1 - [N18000131]NTPC,Karnataka	12/2011	15,166.19 -	12/2016 -	12/2016	0/0
	Total		44,487.16 -			0/0
Railways						
81	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94 604.04	03/1998 08/2005	08/2005	0/0
82	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30	06/2007 -	06/2007	0/0
83	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	07/2008 -	07/2008	0/0
84	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	- 05/2009	05/2009	0/0
85	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36 768.87	- 03/2010	03/2010	0/0
86	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 3,176.10	12/2006 08/2010	08/2010	0/0
87	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	12/2010	0/0
88	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 293.74	12/2010 12/2010	12/2010	0/0
89	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	02/2010 02/2011	02/2011	0/0
90	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 405.17	06/1999 03/2011	03/2011	0/0
91	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	- -	03/2011	0/0
92	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	05/2008 03/2011	03/2011	0/0
93	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	12/2009 03/2011	03/2011	0/0
94	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	- 03/2009	03/2011	0/0
95	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 -	03/2009 12/2009	03/2011	0/0
96	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	03/2011 03/2011	03/2011	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
97	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011	0/0
98	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100007]NCR,Multi State	04/1985	158.77 432.46	03/1994 -	12/2011	0/0
99	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 1,185.00	- 09/2009	12/2011	0/0
100	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	- -	02/2012	0/0
101	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	- 12/2009	02/2012	0/0
102	Dakshin-barasal-lakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	12/2011 02/2012	02/2012	0/0
103	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	- -	03/2012	0/0
104	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	02/2009 -	03/2012	0/0
105	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	- -	03/2012	0/0
106	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	- -	03/2012	0/0
107	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 381.17	- -	03/2012	0/0
108	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	- -	03/2012	0/0
109	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	- -	03/2012	0/0
110	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	03/2010 -	03/2012	0/0
111	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 -	- -	03/2012	0/0
112	MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N22000093]MRTP,Maharashtra	04/2003	3,125.20 4,174.40	06/2011 03/2012	03/2012	0/0
113	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	03/2012 -	03/2012	0/0
114	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	03/2011 -	03/2012	0/0
115	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand	04/2008	167.73 167.73	03/2012 -	03/2012	0/0
116	CHURCHGATE-VIRAR:CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	653.84 1,302.12	06/2013 06/2012	06/2012	0/0
117	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	07/2012 07/2012	07/2012	0/0
118	KADUR-CHIKMAGALUR-SAKLSEHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 333.50	03/2012 03/2012	10/2012	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
119	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 229.88	- -	10/2012	0/0
120	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhandd	04/1997	194.07 194.07	06/2004 -	12/2012	0/0
121	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	03/2012 03/2012	12/2012	0/0
122	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 2,363.00	03/2009 12/2012	12/2012	0/0
123	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 2,921.00	10/2007 12/2012	12/2012	0/0
124	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	03/2010 -	12/2012	0/0
125	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	- -	12/2012	0/0
126	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	- -	01/2013	0/0
127	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44 576.27	12/2012 01/2013	01/2013	0/0
128	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	03/2012 08/2012	02/2013	0/0
129	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	02/2011 02/2011	02/2013	0/0
130	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	12/2012 12/2012	02/2013	0/0
131	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	- -	02/2013	0/0
132	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	03/1995 -	03/2013	0/0
133	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.98	03/2002 -	03/2013	0/0
134	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhandd	04/1995	184.00 900.05	12/2011 12/2011	03/2013	0/0
135	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 1,010.00	- -	03/2013	0/0
136	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	- -	03/2013	0/0
137	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	- -	03/2013	0/0
138	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	- -	03/2013	0/0
139	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	- -	03/2013	0/0
140	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	03/2012 03/2013	03/2013	0/0
141	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 915.70	- -	03/2013	0/0
142	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	- -	03/2013	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
143	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	03/2012 03/2013	03/2013	0/0
144	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 603.04	03/2012 -	03/2013	0/0
145	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	03/2014 -	03/2013	0/0
146	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	02/2009 02/2009	04/2013	0/0
147	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	03/2009 03/2009	04/2013	0/0
148	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 207.52	12/2012 -	05/2013	0/0
149	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	12/2011 11/2013	11/2013	0/0
150	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	- -	12/2013	0/0
151	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 261.70	02/2006 -	12/2013	0/0
152	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	03/2009 -	12/2013	0/0
153	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 401.81	03/2004 12/2010	03/2014	0/0
154	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 733.00	12/2008 -	03/2014	0/0
155	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	- -	03/2014	0/0
156	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	06/2013 06/2013	03/2014	0/0
157	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 200.00	- -	03/2014	0/0
158	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 813.34	03/2014 -	03/2014	0/0
159	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	03/2013 -	03/2014	0/0
160	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 653.19	03/2014 -	03/2014	0/0
161	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 516.23	03/2014 -	03/2014	0/0
162	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	12/2012 -	03/2014	0/0
163	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00 -	03/2010 06/2014	06/2014	0/0
164	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	- -	03/2015	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
165	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, West Bengal	04/1974	31.42 393.46	03/2007 03/2007	03/2015	0/0
166	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR, Bihar	09/2001	100.00 492.98	12/2010 12/2010	03/2015	0/0
167	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR, Mizoram	04/2008	619.34 619.34	04/2014 -	03/2015	0/0
168	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR, Bihar	04/2008	282.92 282.92	- -	03/2015	0/0
169	Himmatnagar - Udaipur Gauge Conversion (NWR) - [N22000112]NWR, Rajasthan	04/2008	829.74 829.74	03/2015 -	03/2015	0/0
170	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR, Nagaland	04/2006	850.00 850.00	03/2015 -	03/2015	0/0
171	BPUTRA BRIDGE AT BOGIBIL & LINK LINES, NEFR - [220100201]NEFR, Assam	09/1997	1,000.00 1,500.00	04/2008 03/2014	12/2015	0/0
172	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL, West Bengal	09/2007	252.50 529.23	02/2010 -	12/2015	0/0
173	SEVOK RANGPO, NEFR - [N22000102]NEFR, Sikkim	04/2008	1,339.48 -	12/2015 -	12/2015	0/0
174	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR, Manipur	04/2003	727.56 727.53	03/2011 03/2014	03/2016	0/0
175	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, Maharashtra	04/2008	5,300.00 -	03/2014 03/2016	03/2016	0/0
176	New Work for Construction of Metro railway from No - [N22000108]RVNL, West Bengal	04/2010	2,397.72 228.82	03/2016 -	03/2016	0/0
177	New Work for Construction of Metro railway from Ba - [N22000109]RVNL, West Bengal	04/2010	2,069.60 -	03/2014 03/2016	03/2016	0/0
178	New Work for Construction of Metro railway from NS - [N22000110]RVNL, West Bengal	04/2010	3,951.98 -	03/2016 -	03/2016	0/0
179	New Work for Construction of Metro railway - [N22000111]RVNL, West Bengal	04/2010	2,619.02 2,913.51	03/2016 -	03/2016	0/0
180	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, West Bengal	03/1998	111.90 1,028.05	03/2005 12/2008	06/2016	0/0
181	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, West Bengal	03/1984	293.97 1,025.39	06/2005 07/2011	06/2016	0/0
182	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133](NR), J and K	03/1995	2,500.00 2,500.00	03/2001 -	12/2017	0/0
183	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL, Chhatisgarh	04/1995	304.00 -	12/2012 -	-	0/0
184	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, Multi State	02/1997	386.30 1,038.00	03/1998 -	-	0/0
185	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR, Kerala	10/1998	550.00 -	- -	-	0/0
186	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL, Andhra Pradesh	06/2000	168.34 -	04/2003 03/2010	-	0/0
187	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR, Andhra Pradesh	12/2001	330.00 1,047.00	- -	-	0/0
188	KODERMA-TILAIYA (NL), ECR - [220100305]ECR, Jharkhand	04/2002	459.91 418.17	- -	-	0/0
189	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, Orissa	04/1998	183.23 -	02/2015 -	-	0/0

(Aug,2012)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
190	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-	0/0
191	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	- -	-	0/0
192	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	- 03/2010	-	0/0
193	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00 -	- -	-	0/0
194	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhand	03/1999	491.19 2,957.21	07/2005 -	07/2005	0/0
195	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 100.00	- -	-	0/0
196	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 901.62	- -	-	0/0
197	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	- -	03/2015	0/0
198	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar	04/2001	104.79 -	- -	-	0/0
199	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	- -	-	0/0
200	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	- -	-	0/0
201	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	- -	-	0/0
202	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 227.40	- -	-	0/0
203	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 582.83	- -	-	0/0
204	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.14 404.39	03/2013 -	03/2013	0/0
205	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24 -	03/2012 -	03/2012	0/0
206	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	03/2011 -	03/2011	0/0
	Total		64,195.28 -			0/0
Road Transport & Highways						
207	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00 -	04/2004 -	09/2012	0/0
208	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI,Uttar Pradesh	12/2003	275.00 -	09/2007 -	09/2012	0/0
209	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	09/2007 -	09/2012	0/0
210	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	06/2005 -	09/2012	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
211	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	10/2008 -	09/2012	0/0
212	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82 -	11/2008 -	09/2012	0/0
213	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27 -	02/2004 -	09/2012	0/0
214	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70 -	02/2004 -	09/2012	0/0
215	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10 -	09/2012 -	09/2012	0/0
216	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00 -	05/2012 -	09/2012	0/0
217	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI,Andhra Pradesh	08/2010	388.00 -	05/2012 -	09/2012	0/0
218	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56 -	02/2012 -	09/2012	0/0
219	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	08/2004 07/2010	10/2012	0/0
220	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	08/2004 -	10/2012	0/0
221	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49 -	03/2005 -	10/2012	0/0
222	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J and K	12/2003	166.27 -	03/2008 -	10/2012	0/0
223	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI,Uttar Pradesh	12/2003	151.30 -	10/2008 -	10/2012	0/0
224	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60 -	06/2010 -	10/2012	0/0
225	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52 -	06/2011 -	10/2012	0/0
226	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75 -	08/2011 -	10/2012	0/0
227	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI,Andhra Pradesh	04/2010	1,740.00 -	10/2012 -	10/2012	0/0
228	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	06/2009 -	11/2012	0/0
229	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45 -	11/2012 -	11/2012	0/0
230	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68 -	03/2008 -	12/2012	0/0
231	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00 -	01/2009 -	12/2012	0/0
232	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00 -	06/2008 -	12/2012	0/0
233	BIJNI TO ASSAM/WB BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	06/2008 -	12/2012	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
234	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94 -	09/2008 -	12/2012	0/0
235	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43 -	10/2008 -	12/2012	0/0
236	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	10/2008 -	12/2012	0/0
237	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI,Madhya pradesh	12/2003	229.91 -	10/2008 -	12/2012	0/0
238	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	07/2008 -	12/2012	0/0
239	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar	12/2003	340.00 -	09/2008 -	12/2012	0/0
240	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00 -	06/2008 -	12/2012	0/0
241	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96 -	04/2008 -	12/2012	0/0
242	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16 -	04/2008 -	12/2012	0/0
243	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00 -	04/2008 -	12/2012	0/0
244	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00 -	12/2008 -	12/2012	0/0
245	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	04/2010 -	12/2012	0/0
246	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93 -	10/2009 -	12/2012	0/0
247	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00 -	12/2009 -	12/2012	0/0
248	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06 -	09/2009 -	12/2012	0/0
249	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45 -	09/2010 -	12/2012	0/0
250	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI,Chhatisgarh	01/2008	464.00 -	01/2011 -	12/2012	0/0
251	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00 -	05/2010 -	12/2012	0/0
252	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00 -	07/2012 -	12/2012	0/0
253	MP/Maharashtra Border-Dhula - [N24000126]NHAI,Maharashtra	12/2009	835.00 -	06/2012 -	12/2012	0/0
254	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70 -	10/2011 -	12/2012	0/0
255	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06 -	12/2012 -	12/2012	0/0
256	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhand	08/2010	625.07 -	01/2013 -	01/2013	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
257	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00 -	01/2011 -	02/2013	0/0
258	PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar	08/2010	671.30 -	02/2013 -	02/2013	0/0
259	JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan	08/2010	267.81 -	02/2013 -	02/2013	0/0
260	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47 -	09/2007 -	03/2013	0/0
261	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00 -	09/2008 -	03/2013	0/0
262	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	05/2008 -	03/2013	0/0
263	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00 -	10/2008 -	03/2013	0/0
264	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	04/2009 -	03/2013	0/0
265	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	06/2008 -	03/2013	0/0
266	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	06/2008 -	03/2013	0/0
267	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00 -	03/2008 -	03/2013	0/0
268	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00 -	06/2008 -	03/2013	0/0
269	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00 -	05/2008 -	03/2013	0/0
270	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	06/2008 -	03/2013	0/0
271	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00 -	09/2007 -	03/2013	0/0
272	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00 -	07/2010 -	03/2013	0/0
273	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00 -	03/2013 -	03/2013	0/0
274	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55 -	03/2013 -	03/2013	0/0
275	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,Gujarat	09/2010	805.39 -	03/2013 -	03/2013	0/0
276	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,Multi State	09/2011	754.00 -	03/2013 -	03/2013	0/0
277	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh	10/2010	1,175.00 -	04/2013 -	04/2013	0/0
278	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	02/2009 05/2014	05/2013	0/0
279	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00 -	05/2013 -	05/2013	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
280	Trichy Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00 -	05/2013 -	05/2013	0/0
281	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16 -	09/2007 -	06/2013	0/0
282	Chikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30 -	10/2011 -	06/2013	0/0
283	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00 -	11/2012 -	06/2013	0/0
284	MURADABAD-BAREILY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00 -	06/2013 -	06/2013	0/0
285	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50 -	06/2013 -	06/2013	0/0
286	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu	06/2011	600.00 -	06/2013 -	06/2013	0/0
287	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81 -	04/2009 -	07/2013	0/0
288	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04 -	11/2008 -	07/2013	0/0
289	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	953.00 -	07/2013 -	07/2013	0/0
290	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88 -	07/2013 -	07/2013	0/0
291	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,Bihar	01/2011	575.00 -	07/2013 -	07/2013	0/0
292	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00 -	11/2011 -	08/2013	0/0
293	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat	03/2011	785.50 -	08/2013 -	08/2013	0/0
294	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00 -	08/2013 -	08/2013	0/0
295	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00 -	08/2013 -	08/2013	0/0
296	BHUBANESWAR TO PURI - [N24000195]NHAI,Orissa	03/2011	500.29 -	08/2013 -	08/2013	0/0
297	4-laning of Faraka-Raiganj - [N24000202]NHAI,Multi State	02/2011	1,078.84 -	08/2013 -	08/2013	0/0
298	4-laning of Brahampore-Faraka - [N24000203]NHAI,Multi State	02/2011	998.79 -	08/2013 -	08/2013	0/0
299	4-laning of Raiganj-Dalkola - [N24000204]NHAI,Multi State	02/2011	580.43 -	08/2013 -	08/2013	0/0
300	New 4 Lane elevated road from chennai airport - [N24000139]NHAI,Tamil Nadu	09/2010	1,655.00 -	09/2013 -	09/2013	0/0
301	BAREILY-SITAPUR - [N24000200]NHAI,Uttar Pradesh	03/2011	1,046.00 -	09/2013 -	09/2013	0/0
302	Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00 -	05/2012 -	10/2013	0/0
303	Tirupati - Chennai - [N24000178]NHAI,Tamil Nadu	04/2011	571.00 -	10/2013 -	10/2013	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
304	BHOPAL-SANCHI - [N24000192]NHAI,Madhya pradesh	10/2011	209.00 -	01/2013 -	10/2013	0/0
305	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00 -	11/2013 -	11/2013	0/0
306	ROHTAK-BAWAL - [N24000169]NHAI,Haryana	05/2011	650.00 -	11/2013 -	11/2013	0/0
307	Muzafarpur - Sonbarsa - [N24000174]NHAI,Bihar	05/2011	511.54 -	11/2013 -	11/2013	0/0
308	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,Bihar	05/2011	511.54 -	11/2013 -	11/2013	0/0
309	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	02/2010 -	12/2013	0/0
310	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI,Tamil Nadu	06/2011	535.00 -	12/2013 -	12/2013	0/0
311	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM. - [N24000172]NHAI,Tamil Nadu	09/2011	1,250.00 -	12/2013 -	12/2013	0/0
312	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	11/2008 -	01/2014	0/0
313	JORBAT - BARAPANI - [N24000180]NHAI,Meghalaya	01/2011	536.00 -	01/2014 -	01/2014	0/0
314	PUNE-SHOLAPUR,Pkg-II - [N24000193]NHAI,Maharashtra	09/2011	835.00 -	01/2014 -	01/2014	0/0
315	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,Orissa	07/2011	586.00 -	01/2014 -	01/2014	0/0
316	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,Uttar Pradesh	07/2012	291.36 -	01/2014 -	01/2014	0/0
317	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00 -	05/2013 -	02/2014	0/0
318	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,Meghalaya	02/2011	226.00 -	02/2014 -	02/2014	0/0
319	4-laning of Barhi-Hazaribagh - [N24000191]NHAI,Jharkhand	02/2012	398.00 -	02/2014 -	02/2014	0/0
320	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00 -	10/2008 -	03/2014	0/0
321	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37 -	10/2011 -	03/2014	0/0
322	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00 -	08/2012 -	03/2014	0/0
323	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54 -	05/2013 -	03/2014	0/0
324	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,Multi State	09/2011	2,848.00 -	03/2014 -	03/2014	0/0
325	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,Bihar	09/2011	574.00 -	03/2014 -	03/2014	0/0
326	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	07/2009 -	04/2014	0/0
327	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00 -	02/2014 -	04/2014	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
328	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,Bihar	10/2011	375.09 -	04/2014 -	04/2014	0/0
329	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI,Andhra Pradesh	11/2011	1,535.00 -	05/2014 -	05/2014	0/0
330	2laning with PS Gopalganj-Chappra - [N24000190]NHAI,Bihar	12/2011	325.00 -	05/2014 -	05/2014	0/0
331	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,Orissa	11/2011	909.00 -	05/2014 -	05/2014	0/0
332	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,J and K	07/2010	1,813.76 -	07/2013 -	06/2014	0/0
333	SNG toBANL - [N24000189]NHAI,J and K	06/2011	1,100.70 -	06/2014 -	06/2014	0/0
334	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,Rajasthan	12/2011	2,388.00 -	06/2014 -	06/2014	0/0
335	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]NHAI,Multi State	12/2011	1,047.00 -	06/2014 -	06/2014	0/0
336	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00 -	09/2013 -	07/2014	0/0
337	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,West Bengal	02/2012	702.16 -	07/2014 -	07/2014	0/0
338	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	08/2014 -	08/2014	0/0
339	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	09/2009 -	09/2014	0/0
340	PANIKHOLI-RIMOLI - [N24000197]NHAI,Orissa	03/2012	1,410.00 -	09/2014 -	09/2014	0/0
341	PANIPAT-ROHTAK - [N24000151]NHAI,Haryana	04/2011	807.00 -	10/2014 -	10/2014	0/0
342	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,Maharashtra	04/2012	484.19 -	10/2014 -	10/2014	0/0
343	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00 -	02/2010 -	12/2014	0/0
344	NASHRI CHANANI - [N24000162]NHAI,J and K	06/2010	2,159.00 -	06/2015 -	05/2016	0/0
345	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,J and K	07/2010	1,987.00 -	07/2015 -	06/2016	0/0
	Total		88,183.22 -			0/0
Shipping & Ports						
346	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 1,571.60	10/2008 -	10/2008	0/0
347	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	04/2009 11/2009	02/2011	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
348	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	03/2012 -	03/2012	0/0
349	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91 -	09/2012 -	09/2012	0/0
350	Acquisition of two nos. of 120 B.P BY 079& 080 - [N25000042]SHIPP.,Maharashtra	04/2009	290.85 -	06/2011 09/2012	09/2012	0/0
351	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	12/2011 09/2012	09/2012	0/0
352	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	04/2011 10/2012	10/2012	0/0
353	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	06/2010 -	11/2012	0/0
354	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	02/2011 -	12/2012	0/0
355	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	01/2012 09/2012	12/2012	0/0
356	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	03/2011 -	03/2013	0/0
357	Setting up of Single Point Mooring (SPM) and allie - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -	05/2013 -	03/2013	0/0
358	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 627.64	12/2012 05/2013	05/2013	0/0
359	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 600.00	03/2006 06/2013	06/2013	0/0
360	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	12/2010 09/2012	10/2013	0/0
361	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	12/2013 -	10/2013	0/0
362	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	02/2014 -	02/2014	0/0
363	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	10/2008 -	-	0/0
	Total		16,087.68 -			0/0
Telecommunications						
364	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84 -	10/2009 -	03/2011	0/0
365	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00 -	12/2005 03/2008	11/2012	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
366	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 930.60	11/2010 -	11/2012	0/0
367	NIB Project Capacity Expansion - [N26000098]BSNL,Multi State	06/2007	175.52 -	12/2008 -	11/2012	0/0
368	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	12/2008 -	12/2012	0/0
369	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	06/2009 -	12/2012	0/0
370	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL,Jharkhandd	03/2008	328.13 -	03/2009 -	12/2012	0/0
371	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	02/2007 03/2012	02/2013	0/0
372	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	01/2009 -	03/2013	0/0
373	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	10/2010 03/2012	03/2013	0/0
374	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38 -	10/2007 -	-	0/0
375	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00 -	03/2009 -	-	0/0
376	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	03/2010 -	-	0/0
377	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	02/2007 12/2010	-	0/0
378	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	03/2010 -	-	0/0
	Total		6,161.00 -			0/0
Urban Development						
379	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00 -	09/2014 -	09/2014	0/0
380	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00 -	03/2016 -	03/2016	0/0
381	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	04/2009 -	-	0/0
	Total		37,850.18 -			0/0
Water Resources						
382	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	12/2007 -	12/2012	0/0
	Total		542.90 -			0/0
Grand Total			373,940.18			0/0

List of Delay Project w.r.t. Original and Revised

(Aug,2012)

						Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
<u>Atomic Energy</u>									
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00 -	17,270.00	14,945.00	12/2008 -	03/2013	51	-
2	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00 -	11,459.00	1,826.00	12/2015 -	11/2016	11	-
3	RAJASTHAN ATOMIC POWER PROJECT -7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00 -	12,320.00	1,158.00	12/2016 -	03/2017	3	-
Total			36,950.00 -	41,049.00	17,929.00				
<u>Civil Aviation</u>									
4	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	2,325.00	2,081.48	05/2011 03/2012	10/2012	17	7
5	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61 -	335.61	130.41	05/2012 -	12/2012	7	-
6	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	309.46	185.18	01/2011 04/2013	04/2013	27	0
Total			2,587.58 -	2,970.07	2,397.07				
<u>Coal</u>									
7	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 3,027.59	3,027.59	2,460.35	06/2009 -	03/2013	45	-
8	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhand	04/2006	471.66 341.63	341.63	108.37	03/2011 -	03/2013	24	-
9	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Uttar Pradesh	05/2006	789.88 741.62	741.62	334.32	03/2010 -	03/2013	36	-
10	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97 -	418.97	95.86	03/2012 -	03/2013	12	-

(Aug,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
11	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19 -	181.19 -	39.22	03/2012 -	03/2013	12	-
12	Tapin OCP - [N06000086]CCL,Jharkhand	08/2008	264.68 -	264.68 -	104.74	03/2012 -	03/2013	12	-
13	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Orissa	01/2005	302.96 -	302.96 -	105.43	03/2010 -	03/2014	48	-
14	TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 -	4,909.54 -	3,296.75	03/2012 -	03/2014	24	-
15	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Orissa	08/2008	207.28 -	207.28 -	100.35	03/2012 -	03/2014	24	-
16	Churi Benti UG - [N06000083]CCL,Jharkhand	06/2007	163.51 -	163.51 -	34.46	03/2011 -	03/2014	36	-
17	North Urimari OCP - [N06000084]CCL,Jharkhand	12/2007	179.87 -	179.87 -	60.69	03/2012 -	03/2014	24	-
18	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	09/2006	212.34 779.26	779.26	310.04	03/2013 09/2012	10/2014	19	25
19	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04 535.10	535.10	162.00	03/2012 03/2015	03/2015	36	0
20	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18 -	287.17 -	0.82	03/2011 -	03/2015	48	-
21	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40 -	259.40 -	1.20	03/2012 -	03/2015	36	-
22	BALRAM OCP EXTENSION,MCL (8.00 Mty) - [N06000044]MCL,Orissa	12/2007	172.08 -	172.08 -	117.83	03/2010 -	03/2015	60	-
23	KAKATIYA LAONGWALL - [N06000048]SCCL,Multi State	12/2008	453.63 -	453.63 -	72.70	12/2012 -	03/2015	27	-
24	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]NCL,Madhya pradesh	05/2006	1,352.04 1,143.54	1,143.54	357.39	03/2014 03/2016	03/2016	24	0
25	MAGADH OC (CCL) - [N06000015]CCL,Jharkhand	07/2006	469.78 -	706.40 -	19.23	07/2012 -	03/2016	44	-

(Aug,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
26	CHURCHA ROUG (1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35	462.35	263.01	03/2014	03/2016	24	-
27	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77	339.77	0.83	03/2014	03/2016	24	-
28	KARTALI (EAST) OCP(2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44	178.44	-	03/2014	03/2016	24	-
29	JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh	09/2008	152.43	152.43	-	03/2015	03/2017	24	-
30	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu	06/2011	5,907.11	5,907.11	22.16	12/2015	08/2017	20	-
Total			20,907.91	22,115.52	8,067.75				
<u>Steel</u>									
31	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89	607.17	339.69	12/2011	10/2012	10	7
32	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00	350.00	246.19	08/2010	10/2012	26	26
33	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	08/2007	108.00	216.68	91.83	10/2012	12/2012	2	2
34	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00	16,408.00	13,628.33	12/2011	12/2012	12	-
35	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhand	01/2008	6,325.00	6,325.00	2,874.30	12/2011	12/2012	12	-
36	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00	343.58	248.53	02/2011	12/2012	22	22
37	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00	450.00	205.20	05/2012	02/2013	9	9

(Aug,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
38	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00 12,291.00	12,291.00	9,726.00	10/2009 03/2013	03/2013	41	0
39	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,West Bengal	06/2009	2,875.00 -	2,875.00	1,062.04	12/2012 -	03/2013	3	-
40	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	17,265.00 -	17,265.00	6,043.92	03/2013 -	09/2013	6	-
41	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON - [N12000075]SAIL,Orissa	11/2011	254.55 -	254.55	11.38	11/2013 -	03/2014	4	-
Total			51,228.44 -	57,385.98	34,477.41				
<u>Petroleum</u>									
42	COMPRESSOR STATIONS (KAILARAS AND CHAINSA) - [N16000054]GAIL,Multi State	11/2007	1,167.00 -	798.00	732.04	04/2011 12/2011	09/2012	17	9
43	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	1,282.33	09/2011 03/2012	09/2012	12	6
44	KOCHI-KOOTANAD BANGALORE-MANGALORE PIPELINE PROJEC - [N16000071]GAIL,Multi State	06/2009	348.00 -	261.00	196.33	03/2012 08/2012	09/2012	6	1
45	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32 -	330.47	218.92	03/2012 -	09/2012	6	-
46	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	5,557.03	05/2010 05/2012	10/2012	29	5
47	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11 -	370.11	249.90	04/2011 -	10/2012	18	-
48	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 12,160.26	12,160.26	8,984.37	01/2012 -	11/2012	10	-
49	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State	06/2009	4,543.43 4,508.38	2,300.00	1,869.00	03/2012 08/2012	12/2012	9	4

(Aug,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
50	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	977.00	479.00	12/2011 -	01/2013	13	-
51	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	269.29	03/2006 03/2013	03/2013	84	0
52	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	7,084.38	05/2010 03/2013	03/2013	34	0
53	INTEGRATED OFFSHORE CRUDE OIL HANDLING FACILITIES - [N16000090]IOCL,Orissa	12/2009	1,492.33 -	1,492.33	1,164.57	06/2012 03/2013	03/2013	9	0
54	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	755.76	677.99	03/2011 05/2011	03/2013	24	22
55	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	288.04	154.37	08/2012 -	03/2013	7	-
56	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	04/2013	52	0
57	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,858.42	09/2010 03/2012	04/2013	31	13
58	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	1,803.78	613.33	07/2012 -	04/2013	9	-
59	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	61.66	03/2013 -	04/2013	1	-
60	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	479.11	03/2010 03/2012	05/2013	38	14
61	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	868.04	07/2010 05/2012	05/2013	34	12
62	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	06/2013	86	12

(Aug,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
63	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64	2,163.64	1,140.31	06/2012	06/2013	12	-
64	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92	460.70	250.95	07/2012	06/2013	11	11
65	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00	1,000.00	186.44	01/2013	06/2013	5	-
66	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26	240.95	43.73	09/2012	06/2013	9	-
67	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65	736.65	287.21	09/2011	08/2013	23	-
68	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39	6,855.93	4,060.65	09/2012	09/2013	12	-
69	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44	410.44	43.99	11/2012	10/2013	11	-
70	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00	820.00	-	06/2012	10/2013	16	-
71	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64	723.64	-	03/2013	11/2013	8	-
72	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78	5,633.44	3,761.86	08/2010	12/2013	40	21
73	KOCHI KOOTTANAD BANGLORE MANGLORE PIPELINE PH-II - [N16000129]GAIL,Multi State	06/2009	2,915.00	2,915.00	1,057.23	12/2012	12/2013	12	12
74	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20	269.10	-	08/2013	01/2014	5	-
75	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10	663.69	629.66	03/2007	03/2014	84	0
76	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15	2,378.86	938.59	03/2013	03/2014	12	-

(Aug,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
77	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03	3,241.03	356.20	03/2013	04/2014	13	-
78	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07	281.07	3.48	10/2010	12/2014	50	-
79	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18	7,596.18	2.20	01/2013	07/2015	30	-
80	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09	1,674.11	1,535.19	03/2007	03/2017	120	0
	Total		80,979.54	89,805.02	51,802.68				
	<u>Power</u>								
81	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J and K	08/2006	621.26	913.00	751.21	02/2011	10/2012	20	0
82	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36	1,736.36	994.40	06/2012	10/2012	4	-
83	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34	232.34	112.28	06/2012	10/2012	4	-
84	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61	276.61	158.30	04/2012	10/2012	6	-
85	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37	386.32	328.83	07/2011	11/2012	16	-
86	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32	1,347.32	1,067.60	02/2012	11/2012	9	-
87	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29	2,159.07	1,833.11	09/2008	12/2012	51	-
88	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23	5,221.23	3,153.00	07/2010	12/2012	29	-

(Aug,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
89	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	1,075.12	640.00	05/2012 -	12/2012	7	-
90	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83 -	1,216.83	739.30	08/2012 -	12/2012	4	-
91	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92 -	1,628.00	1,551.34	03/2007 09/2012	01/2013	70	4
92	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J and K	08/2006	611.01 -	936.00	786.38	08/2010 01/2013	01/2013	29	0
93	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24 -	758.75	589.00	01/2010 -	02/2013	37	-
94	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J and K	08/2005	1,729.29 -	2,083.00	1,772.30	11/2009 02/2013	03/2013	40	1
95	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96 -	975.96	867.25	10/2009 -	03/2013	41	-
96	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28 -	6,010.89	4,349.00	08/2012 -	03/2013	7	-
97	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	151.20	11/2011 -	03/2013	16	-
98	SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95 -	2,360.95	1,948.00	08/2012 -	03/2013	7	-
99	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	5,319.00	08/2012 -	03/2013	7	-
100	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00 -	5,915.00	3,767.00	10/2012 -	03/2013	5	-

(Aug, 2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
101	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL, Multi State	02/2010	2,144.00 -	2,144.00	886.40	12/2012 -	03/2013	3	-
102	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL, Multi State	03/2010	965.58 -	965.58	437.00	11/2012 -	03/2013	4	-
103	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL, Multi State	10/2010	160.32 -	160.32	48.80	10/2012 -	03/2013	5	-
104	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC, Uttar Pradesh	01/2009	6,230.81 -	6,230.81	3,475.00	10/2012 -	05/2013	7	-
105	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC, Himachal Pr.	10/2005	2,304.56 -	2,716.00	1,893.71	10/2010 01/2013	06/2013	32	5
106	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL, Multi State	03/2010	4,672.99 -	4,672.99	1,505.60	11/2012 -	06/2013	7	-
107	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC, West Bengal	09/2005	1,061.38 -	1,501.75	1,173.29	09/2009 06/2013	08/2013	47	2
108	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pr.	01/2007	2,047.03 -	2,047.03	1,914.62	01/2012 -	09/2013	20	-
109	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL, Multi State	10/2008	4,824.12 -	4,824.12	2,896.40	10/2012 -	09/2013	11	-
110	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL, Multi State	08/2010	1,677.57 -	1,677.57	512.00	04/2013 -	10/2013	6	-
111	Transmission system for transfer of power from Gen. - [N18000098]PGCIL, Multi State	05/2010	250.03 -	250.03	56.90	01/2013 -	11/2013	10	-

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
112	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	316.20	11/2011 -	12/2013	25	-
113	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	335.80	11/2011 -	12/2013	25	-
114	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	241.00	02/2012 -	12/2013	22	-
115	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pr.	10/2002	4,527.15 -	4,527.15	4,448.00	04/2009 03/2014	03/2014	59	0
116	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	1,272.80	384.60	11/2012 -	03/2014	16	-
117	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04 -	7,341.04	4,551.00	08/2013 -	06/2014	10	-
118	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pr.	12/2008	573.99 -	573.99	383.57	08/2012 08/2013	09/2014	25	13
119	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	4,951.10	08/2013 -	09/2014	13	-
120	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	3,250.00	07/2011 -	11/2014	40	-
121	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,Mizoram	01/2011	913.63 913.63	913.63	344.41	07/2014 02/2015	02/2015	7	0
122	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00 2,978.86	2,978.86	371.17	07/2010 02/2016	02/2016	67	0
123	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97 -	8,693.00	7,288.00	12/2009 12/2014	03/2016	75	15
124	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttaranchal	08/2008	2,491.58 2,491.58	3,422.44	316.25	07/2014 -	05/2016	22	-

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
125	KISHANGANGA HEP - [N18000031]NHPC,J and K	07/2007	2,238.67 3,642.04	3,642.00	1,630.50	01/2016 01/2016	11/2016	10	10
126	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pr.	09/2003	6,285.33 -	10,667.00	5,733.74	09/2010 08/2014	03/2017	78	31
127	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pr.	12/2004	2,496.90 -	2,496.90	1,954.52	05/2013 06/2016	03/2017	46	9
128	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pr.	09/2002	3,919.59 -	5,366.00	3,532.32	09/2009 07/2014	12/2017	99	41
Total			125,135.91	138,523.25	85,710.40				
<u>Railways</u>									
129	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 333.50	333.50	210.82	03/2012 03/2012	10/2012	7	7
130	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 194.07	456.45	293.29	06/2004 -	12/2012	102	-
131	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	500.00	414.03	03/2012 03/2012	12/2012	9	9
132	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]JECR,Bihar	04/2002	921.00 2,363.00	2,363.00	792.32	03/2009 12/2012	12/2012	45	0
133	PATNA GANGA BRIDGE (NL), ECR - [220100308]JECR,Bihar	04/2001	624.47 2,921.00	2,921.00	1,514.74	10/2007 12/2012	12/2012	62	0
134	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya Pradesh	09/2007	687.20 -	687.20	656.89	03/2010 -	12/2012	33	-
135	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44 576.27	1,115.21	877.21	12/2012 01/2013	01/2013	1	0
136	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]JECR,Bihar	04/1997	233.00 501.69	1,043.55	659.06	03/2012 08/2012	02/2013	11	6
137	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	270.00	260.85	02/2011 02/2011	02/2013	24	24
138	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	607.09	407.33	12/2012 12/2012	02/2013	2	2

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
139	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	634.13	555.27	03/1995 -	03/2013	216	-
140	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.98	227.94	202.02	03/2002 -	03/2013	132	-
141	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 900.05	900.05	565.12	12/2011 12/2011	03/2013	15	15
142	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	341.41	272.26	03/2012 03/2013	03/2013	12	0
143	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	477.88	392.05	03/2012 03/2013	03/2013	12	0
144	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 603.04	603.04	96.76	03/2012 -	03/2013	12	-
145	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	243.40	248.79	02/2009 02/2009	04/2013	50	50
146	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	225.00	212.13	03/2009 03/2009	04/2013	49	49
147	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 207.52	207.52	137.67	12/2012 -	05/2013	5	-
148	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	611.03	105.94	12/2011 11/2013	11/2013	23	0
149	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 261.70	261.70	56.12	02/2006 -	12/2013	94	-
150	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	4,255.37	3,161.45	03/2009 -	12/2013	57	-
151	BELAPUR-SEAWOOD-URAN ELECTRI-IED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 401.81	495.44	191.30	03/2004 12/2010	03/2014	120	39
152	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 733.00	1,655.81	1,275.88	12/2008 -	03/2014	63	-
153	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	495.74	162.22	06/2013 06/2013	03/2014	9	9

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
154	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	482.70	384.35	03/2013 -	03/2014	12	-
155	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	223.01	108.83	12/2012 -	03/2014	15	-
156	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00 -	820.40	150.01	03/2010 06/2014	06/2014	51	0
157	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	499.16	168.27	03/2007 03/2007	03/2015	96	96
158	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,041.79	730.92	12/2010 12/2010	03/2015	51	51
159	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 619.34	2,393.48	11.78	04/2014 -	03/2015	11	-
160	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	3,230.01	2,408.10	04/2008 03/2014	12/2015	92	21
161	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 529.23	529.23	225.10	02/2010 -	12/2015	70	-
162	JIRIBAM TO IMPHAL (TUPU)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	4,444.00	911.23	03/2011 03/2014	03/2016	60	24
163	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	5,300.00	850.42	03/2014 03/2016	03/2016	24	0
164	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,069.60	27.66	03/2014 03/2016	03/2016	24	0
165	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,028.05	1,412.74	448.10	03/2005 12/2008	06/2016	135	90
166	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	1,086.41	426.22	06/2005 07/2011	06/2016	132	59
167	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J and K	03/1995	2,500.00 2,500.00	8,000.00	8,069.06	03/2001 -	12/2017	201	-
Total			23,563.11	53,464.99	28,641.57				

(Aug,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
	<u>Road Transport & Highways</u>								
168	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00 -	241.53	132.10	04/2004 -	09/2012	101	-
169	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI,Uttar Pradesh	12/2003	275.00 -	275.00	306.19	09/2007 -	09/2012	60	-
170	HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	220.00	277.83	09/2007 -	09/2012	60	-
171	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	230.00	226.35	06/2005 -	09/2012	87	-
172	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	250.39	279.36	10/2008 -	09/2012	47	-
173	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82 -	221.82	284.81	11/2008 -	09/2012	46	-
174	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27 -	263.27	269.79	02/2004 -	09/2012	103	-
175	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70 -	228.70	189.38	02/2004 -	09/2012	103	-
176	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00 -	795.00	1,023.40	05/2012 -	09/2012	4	-
177	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI,Andhra Pradesh	08/2010	388.00 -	388.00	506.40	05/2012 -	09/2012	4	-
178	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56 -	390.56	631.65	02/2012 -	09/2012	7	-
179	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	196.65	179.66	08/2004 07/2010	10/2012	98	27
180	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	207.56	185.13	08/2004 -	10/2012	98	-
181	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49 -	367.49	453.68	03/2005 -	10/2012	91	-

(Aug,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
182	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J and K	12/2003	166.27	193.10	163.41	03/2008	10/2012	55	-
183	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI,Uttar Pradesh	12/2003	151.30	151.30	190.52	10/2008	10/2012	48	-
184	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI, Madhya pradesh	12/2003	407.60	407.60	185.78	06/2010	10/2012	28	-
185	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI, Maharashtra	04/2010	1,170.52	1,170.52	4.41	06/2011	10/2012	16	-
186	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI, Multi State	02/2009	1,693.75	1,693.75	2,659.00	08/2011	10/2012	14	-
187	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00	280.00	581.49	06/2009	11/2012	41	-
188	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68	340.68	385.28	03/2008	12/2012	57	-
189	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00	190.00	259.75	01/2009	12/2012	47	-
190	DAKOBA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00	225.00	281.21	06/2008	12/2012	54	-
191	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80	237.80	248.21	06/2008	12/2012	54	-
192	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94	332.94	389.13	09/2008	12/2012	51	-
193	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI, Madhya pradesh	12/2003	203.43	203.43	237.75	10/2008	12/2012	50	-
194	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, Madhya pradesh	12/2003	251.03	251.03	309.92	10/2008	12/2012	50	-

(Aug,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
195	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA - [240106305]NHAI, Madhya Pradesh	12/2003	229.91 -	229.91	262.25	10/2008 -	12/2012	50	-
196	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, West Bengal	12/2003	225.00 -	225.00	183.84	07/2008 -	12/2012	53	-
197	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI, Bihar	12/2003	340.00 -	340.00	541.94	09/2008 -	12/2012	51	-
198	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00 -	200.00	274.19	06/2008 -	12/2012	54	-
199	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, Assam	12/2003	175.96 -	175.96	151.42	04/2008 -	12/2012	56	-
200	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI, Karnataka	04/2000	196.50 363.00	196.50	248.66	06/2011 06/2011	12/2012	18	18
201	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, Assam	12/2003	198.16 -	198.16	210.81	04/2008 -	12/2012	56	-
202	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00 -	208.00	266.19	04/2008 -	12/2012	56	-
203	NAGPUR-KONDHALI, NH-6 (NHA) - [N24000055]NHAI, Maharashtra	03/2005	168.00 -	168.00	457.30	12/2008 -	12/2012	48	-
204	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, Assam	12/2003	217.61 -	217.61	212.06	04/2010 -	12/2012	32	-
205	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI, Madhya Pradesh	12/2003	300.93 -	300.93	302.72	10/2009 -	12/2012	38	-
206	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, Multi State	12/2003	604.00 -	604.00	494.29	12/2009 -	12/2012	36	-
207	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI, Uttar Pradesh	12/2003	355.06 -	355.06	469.55	09/2009 -	12/2012	39	-
208	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI, Multi State	12/2003	232.45 -	232.45	274.33	09/2010 -	12/2012	27	-
209	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI, Chhattisgarh	01/2008	464.00 -	464.00	535.25	01/2011 -	12/2012	23	-
210	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, Haryana	04/2007	486.00 -	486.00	587.32	05/2010 -	12/2012	31	-

(Aug,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
211	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, Maharashtra	03/2005	940.00 -	940.00	1,141.10	07/2012 -	12/2012	5	-
212	MP/Maharashtra Border-Dhula - [N24000126]NHAI, Maharashtra	12/2009	835.00 -	835.00	1,068.70	06/2012 -	12/2012	6	-
213	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI, Multi State	04/2009	1,673.70 -	1,673.70	2,723.00	10/2011 -	12/2012	14	-
214	SALEM - U / UNDRUPET (BOT -1/TN-06) NH -68 - [N24000102]NHAI, Tamil Nadu	03/2005	941.00 -	941.00	1,901.00	01/2011 -	02/2013	25	-
215	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, Assam	12/2003	157.47 -	154.57	201.65	09/2007 -	03/2013	66	-
216	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, Uttar Pradesh	12/2003	155.00 -	201.66	128.88	09/2008 -	03/2013	54	-
217	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI, Punjab	12/2003	284.00 -	359.00	216.44	05/2008 -	03/2013	58	-
218	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI, Bihar	12/2003	240.00 -	240.00	294.12	10/2008 -	03/2013	53	-
219	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, Assam	12/2003	200.00 -	200.00	112.26	04/2009 -	03/2013	47	-
220	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI, Assam	12/2003	195.00 -	195.00	205.46	06/2008 -	03/2013	57	-
221	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, Assam	12/2003	264.72 -	264.72	287.76	06/2008 -	03/2013	57	-
222	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, Assam	12/2003	245.00 -	245.00	491.21	03/2008 -	03/2013	60	-
223	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, Assam	12/2003	225.00 -	225.00	240.75	06/2008 -	03/2013	57	-
224	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, Assam	12/2003	160.00 -	160.00	175.99	05/2008 -	03/2013	58	-

(Aug,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
225	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI, Assam	12/2003	200.00 -	200.00	231.15	06/2008 -	03/2013	57	-
226	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI, Assam	12/2003	212.00 -	386.10	26.30	09/2007 -	03/2013	66	-
227	TRICHY - KORUR NH-67 - [N24000101]NHAI, Tamil Nadu	03/2005	516.00 -	516.00	760.07	07/2010 -	03/2013	32	-
228	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, Assam	12/2003	280.00 -	280.00	271.25	02/2009 05/2014	05/2013	51	-12
229	AGRA-BYPASS(NS-1/UP-1), KM 176.8-13.03 NH-2,3 - [N24000098]NHAI, Uttar Pradesh	12/2003	348.16 -	465.50	178.61	09/2007 -	06/2013	69	-
230	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI, Andhra Pradesh	05/2009	572.30 -	572.30	691.40	10/2011 -	06/2013	20	-
231	AMRITSAR-PATHANKOT - [N24000147]NHAI, Punjab	05/2010	705.00 -	705.00	1,158.30	11/2012 -	06/2013	7	-
232	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, Assam	12/2003	199.81 -	385.13	60.42	04/2009 -	07/2013	51	-
233	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, Assam	12/2003	155.04 -	280.13	92.32	11/2008 -	07/2013	56	-
234	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI, Haryana	05/2009	1,108.00 -	2,288.00	3,460.60	11/2011 -	08/2013	21	-
235	Pune-sholapur, pkg1 - [N24000127]NHAI, Maharashtra	11/2009	1,110.00 -	1,110.00	1,802.10	05/2012 -	10/2013	17	-
236	BHOPAL-SANCHI - [N24000192]NHAI, Madhya pradesh	10/2011	209.00 -	209.00	3.81	01/2013 -	10/2013	9	-
237	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, Rajasthan	12/2003	275.00 -	281.31	179.23	02/2010 -	12/2013	46	-
238	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, Assam	12/2003	167.64 -	167.64	20.73	11/2008 -	01/2014	62	-
239	INDORE-DEWAS(NH-3) - [N24000159]NHAI, Madhya pradesh	11/2010	325.00 -	325.00	376.84	05/2013 -	02/2014	9	-
240	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI, Bihar	12/2003	300.00 -	300.00	175.01	10/2008 -	03/2014	65	-

(Aug,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
241	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37 -	353.37	355.53	10/2011 -	03/2014	29	-
242	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00 -	617.00	154.52	08/2012 -	03/2014	19	-
243	2 LANNING OF MOKAMAMUNGER - [N24000166]NHAI,Bihar	05/2011	351.54 -	351.54	326.19	05/2013 -	03/2014	10	-
244	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	363.74	49.25	07/2009 -	04/2014	57	-
245	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00 -	664.00	211.79	02/2014 -	04/2014	2	-
246	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,J and K	07/2010	1,813.76 -	1,813.76	-	07/2013 -	06/2014	11	-
247	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00 -	359.00	33.82	09/2013 -	07/2014	10	-
248	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	263.17	233.77	09/2009 -	09/2014	60	-
249	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00 -	557.00	930.92	02/2010 -	12/2014	58	-
250	NASHRI CHANANI - [N24000162]NHAI,J and K	06/2010	2,159.00 -	2,159.00	-	06/2015 -	05/2016	11	-
251	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,J and K	07/2010	1,987.00 -	1,987.00	-	07/2015 -	06/2016	11	-
Total			37,210.42 -	39,149.04	37,285.96				
Shipping & Ports									
252	Acquisition of two nos. of 120 B.P BY 079& 080 - [N25000042]SHIPP.,Mahara shtra	04/2009	290.85 -	305.00	197.14	06/2011 09/2012	09/2012	15	0
253	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Mahara shtra	04/2009	277.03 280.00	277.03	188.88	12/2011 09/2012	09/2012	9	0
254	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Mahara shtra	10/2007	359.44 -	359.44	358.78	04/2011 10/2012	10/2012	18	0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
255	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	29	-
256	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012	22	-
257	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	4,150.00	3,433.40	01/2012 09/2012	12/2012	11	3
258	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	24	-
259	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 627.64	627.64	214.65	12/2012 05/2013	05/2013	5	0
260	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 600.00	600.00	110.00	03/2006 06/2013	06/2013	87	0
261	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	841.40	12/2010 09/2012	10/2013	34	13
Total			8,446.14 -	10,038.71	5,564.18				
<u>Telecommunications</u>									
262	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00 -	250.00	80.47	12/2005 03/2008	11/2012	83	56
263	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N260000090]BSNL,Madhya pradesh	11/2009	916.70 930.60	930.60	805.75	11/2010 -	11/2012	24	-
264	NIB Project Capacity Expansion - [N260000098]BSNL,Multi State	06/2007	175.52 -	175.52	60.84	12/2008 -	11/2012	47	-
265	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N260000041]BSNL,Punjab	02/2008	373.94 -	373.94	231.79	12/2008 -	12/2012	48	-

(Aug,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
266	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	158.72	76.70	06/2009 -	12/2012	42	-
267	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL,Jharkhand	03/2008	328.13 -	328.12	164.58	03/2009 -	12/2012	45	-
268	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	229.41	67.20	02/2007 03/2012	02/2013	72	11
269	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	157.98	01/2009 -	03/2013	50	-
270	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	384.00	29.45	10/2010 03/2012	03/2013	29	12
Total			3,163.25 -	3,167.12	1,674.76				
<u>Urban Development</u>									
271	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00 -	11,609.00	2,267.57	12/2011 -	03/2013	15	-
Total			6,395.00 -	11,609.00	2,267.57				
<u>Water Resources</u>									
272	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012	60	-
Total			542.90 -	1,187.00	35.49				
Grand Total			397,110.20	470,464.70	275,853.84				

List of ongoing projects having cost overrun w.r.to original

(Aug,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Atomic Energy</u>						
1	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	14,945.00	12/2008 -	03/2013
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	3,641.60	09/2010 -	01/2012
	Total		16,663.00 -	22,947.00	18,586.60		
	<u>Civil Aviation</u>						
3	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]	08/2008	1,942.51 -	2,325.00	2,081.48	05/2011 -	10/2012
4	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. TER BLDG(K1) [N04000038]	08/2008	1,808.00 -	2,015.00	1,676.63	01/2011 -	02/2012
	Total		3,750.51 -	27,287.00	22,344.71		
	<u>Coal</u>						
5	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,027.59	2,460.35	06/2009 -	03/2013
6	MAGADH OC (CCL) - [N06000015]	07/2006	469.78 -	706.40	19.23	07/2012 -	03/2016
7	ADRIYALA SHAFT PROJECT - [N06000016]	09/2006	212.34 -	779.26	310.04	03/2013 -	10/2014
8	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]	12/2007	490.00 -	490.10	115.68	03/2017 -	03/2017
9	TUTICORIN THERMAL POWER PROJECT - [N06000047]	05/2008	4,904.54 -	4,909.54	3,296.75	03/2012 -	03/2014
10	MANIKPUR OC EXPANSION - [N06000081]	11/2009	321.42 -	321.50	203.67	03/2014 -	03/2014
11	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	84.63	03/2016 -	03/2016
	Total		8,579.45 -	37,719.98	28,835.06		
	<u>Petrochemicals</u>						
12	Assam gas Cracker project - [N16000106]	04/2006	5,460.61 -	8,920.00	5,197.24	12/2013 -	12/2013
	Total		5,460.61 -	46,639.98	34,032.30		
	<u>Petroleum</u>						
13	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]	09/2001	345.10 -	663.69	629.66	03/2007 -	03/2014

(Aug,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
14	IOR GELEKI (ONGCL) - [160100216	09/2001	390.09 -	1,674.11	1,535.19	03/2007 -	03/2017
15	IOR, RUDRASAGAR (ONGCL) - [160100217	09/2001	113.90 -	438.85	269.29	03/2006 -	03/2013
16	DEV OF G1 AND GS-15 (ONGCL) - [160100231	04/2003	429.82 -	2,735.65	2,184.00	04/2006 -	06/2013
17	DEVELOPMENT OF C-SERIES FIELDS - [N16000023	08/2006	3,195.16 -	3,690.37	2,520.91	12/2008 -	04/2013
18	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030	01/2007	2,853.29 -	6,326.40	5,557.03	05/2010 -	10/2012
19	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032	01/2007	2,323.40 -	2,920.82	1,858.42	09/2010 03/2012	04/2013
20	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033	06/2007	3,248.78 -	5,633.44	3,761.86	08/2010 03/2012	12/2013
21	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039	10/2007	5,713.03 -	8,813.41	7,084.38	05/2010 -	03/2013
22	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044	05/2008	333.40 -	656.51	656.90	05/2010 -	07/2012
23	RESITMENT OF MARKETING INSTALATION AT VISAKH [N16000057	01/2009	756.00 -	898.00	893.30	- -	08/2012
24	PARADIP REFINERY PROJECT - [N16000058	02/2009	29,777.00 -	30,426.00	17,280.00	- -	09/2013
25	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI [N16000066	01/2008	224.00 -	394.00	355.45	- -	-
26	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I [N16000070	07/2009	238.68 -	302.00	217.12	- -	10/2012
27	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY [N16000081	04/2008	825.00 -	1,827.00	611.55	04/2013 -	04/2013
28	North Tapti Gas Field Development - [N16000096	07/2008	589.70 755.56	755.76	677.99	03/2011 -	03/2013
	Total		51,356.35 -	114,795.99	80,125.35		
Power							
29	PARBATI HEP (NHPC) II - [180100210	09/2002	3,919.59 -	5,366.00	3,532.32	09/2009 -	12/2017
30	SUBANSIRI LOWER H.E.P (NHPC) - [180100221	09/2003	6,285.33 -	10,667.00	5,733.74	09/2010 -	03/2017
31	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC) [180100222	10/2003	768.92 -	1,628.00	1,551.34	03/2007 -	01/2013
32	BARH STPP(3X660MW) NTPC - [180100242	12/2003	8,692.97 -	8,693.00	7,288.00	12/2009 -	03/2016
33	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243	09/2005	1,061.38 -	1,501.75	1,173.29	09/2009 -	08/2013
34	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246	03/2005	596.45 -	1,007.16	842.33	12/2007 -	-

(Aug,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
35	PARBATI H.E.P. STAGE -III (NHPC) - [180100250	10/2005	2,304.56 -	2,716.00	1,893.71	10/2010 -	06/2013
36	URI H.E.P STAGE -II (NHPC) - [180100251	08/2005	1,729.29 -	2,083.00	1,772.30	11/2009 -	03/2013
37	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258	05/2005	1,779.29 -	2,159.07	1,833.11	09/2008 -	12/2012
38	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006	08/2006	611.01 -	936.00	786.38	08/2010 -	01/2013
39	CHUTAK HYDRO-ELECTRIC PROJECT - [N18000007	08/2006	621.26 -	913.00	751.21	02/2011 -	10/2012
40	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	07/2006	1,657.00 -	2,978.86	371.17	07/2010 -	02/2016
41	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP [N18000018	07/2006	557.24 -	758.75	589.00	01/2010 -	02/2013
42	KISHANGANGA HEP - [N18000031	07/2007	2,238.67 -	3,642.00	1,630.50	01/2016 -	11/2016
43	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT [N18000042	08/2008	2,491.58 -	3,422.44	316.25	07/2014 -	05/2016
44	MOUDA STPP - [N18000048	11/2008	5,459.28 -	6,010.89	4,349.00	08/2012 -	03/2013
45	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064	04/2008	297.37 -	386.32	328.83	07/2011 -	11/2012
46	TRIPURA GAS BASED POWER PROJECT - [N18000071	07/2009	421.01 -	623.44	325.05	- -	07/2013
	Total		41,492.20 -	170,288.67	115,192.88		
<u>Railways</u>							
47	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100007	04/1985	158.77 274.56	540.96	558.07	03/1994 -	12/2011
48	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009	03/1984	520.00 422.79	634.13	555.27	03/1995 -	03/2013
49	VIRAMGAM-BHILDI(WR),GC - [220100062	04/1990	155.66 -	356.87	166.04	- 03/2010	-
50	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	925.30	584.06	- -	03/2012
51	AMRAVATI-NARKHER NL(CR) - [220100118	06/1994	120.90 175.30	548.95	518.45	06/1999 -	03/2011
52	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	8,000.00	8,069.06	03/2001 -	12/2017
53	New BG line Rly line from Eklakhi-Balurghat including Gazole-Itahar(NL),NEFR - [220100135	04/1983	36.80 274.41	703.17	242.01	- -	03/2015
54	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148	04/1993	100.00 119.29	227.94	202.02	03/2002 -	03/2013
55	DALLI-RAJHARA - RAOGHAT(PART OF DALLI- RAJHARA-JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	968.60	110.02	12/2012 -	-
56	CALICUT-MANGALORE (DL) (SR) - [220100151	02/1996	240.00 -	579.37	600.41	- -	02/2012

(Aug,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
57	BELAPUR-SEAWOOD-URAN ELECTRIF-IED DOUBLE LINE(MTP) - [220100164	03/1996	401.81 -	495.44	191.30	03/2004 -	03/2014
58	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168	04/1995	184.00 -	900.05	565.12	12/2011 12/2010	03/2013
59	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181	02/1997	353.08 -	2,200.00	182.53	- -	03/2013
60	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR [220100183	02/1997	295.00 -	944.55	509.89	- -	01/2013
61	DAUSA-GANGAPUR CITY(NL),NWR - [220100184	02/1997	151.84 -	410.08	194.48	- -	03/2013
62	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,038.00	590.26	03/1998 -	-
63	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	37.68 -	730.00	347.70	07/2012 -	07/2012
64	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190	04/1996	157.00 -	333.50	210.82	03/2012 -	10/2012
65	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	712.00	736.89	- -	10/2012
66	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192	03/1996	155.74 164.36	883.00	626.80	02/2009 -	03/2012
67	HUBLI-ANKOLA(NL),SWR - [220100193	04/1995	227.00 -	997.58	69.57	- -	-
68	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197	03/1997	395.00 598.98	1,577.46	1,354.57	- -	03/2012
69	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201	09/1997	1,000.00 -	3,230.01	2,408.10	04/2008 12/2011	12/2015
70	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	645.00	133.87	- -	03/2012
71	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	31.42 154.30	499.16	168.27	03/2007 03/2007	03/2015
72	KOTTUR-HARIHAR(NL),(SWR) - [220100212	04/1995	65.94 -	302.23	336.49	- -	03/2011
73	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	456.45	293.29	06/2004 -	12/2012
74	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	0.35	07/2008 -	07/2008
75	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222	03/1999	491.19 -	2,957.21	1,254.61	07/2005 -	-
76	CHURCHGATE-VIRAR CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233	07/1996	653.84 654.51	1,302.12	608.97	06/2013 -	06/2012
77	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR [220100240	04/1997	233.00 335.77	1,043.55	659.06	03/2012 -	02/2013
78	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241	07/1998	248.44 -	1,115.21	877.21	12/2012 -	01/2013
79	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	227.42	250.82	12/2009 -	03/2011
80	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	100.00 -	1,041.79	730.92	12/2010 -	03/2015

(Aug,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
81	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	550.00 -	1,214.00	96.96	- -	-
82	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	776.00	324.70	- 05/2009	05/2009
83	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR- NAUTANWA GC (NER) [220100255	03/2002	381.17 -	863.23	580.64	- -	03/2012
84	KAPTANGANJ-THAWA-SIWAN-CHHAPRA GC (NER) - [220100256	04/1999	323.40 -	750.89	495.55	- -	03/2014
85	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257	04/1997	78.23 -	162.87	92.71	- -	03/2013
86	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	409.00 408.76	847.76	833.20	06/2007 -	06/2007
87	RENIGUNTA-GUNTAKAL(RE) - [220100260	06/2000	168.34 -	370.00	354.18	04/2003 03/2010	-
88	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	548.96	504.71	- -	-
89	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) - [220100263	03/1998	280.00 -	1,029.00	753.56	- -	03/2013
90	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	330.00 -	1,047.00	9.41	- -	-
91	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	1,655.81	1,275.88	12/2008 -	03/2014
92	TOLLYGANJ-GARIA with extension to Dum Dum- Noapara and Noapara-NSCB Airport(MTP) - [220100268	03/2000	907.69 -	3,176.10	3,205.43	12/2006 -	08/2010
93	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	260.85	02/2011 -	02/2013
94	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	157.96 -	1,188.91	536.08	- 12/2009	02/2012
95	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	138.00 240.59	607.09	407.33	12/2012 12/2012	02/2013
96	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	02/1999	138.00 -	901.62	0.29	- -	-
97	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	1,412.74	448.10	03/2005 12/2008	06/2016
98	REWARI-ROHTAK (NL),NR - [220100279	01/2004	149.38 -	530.76	486.96	02/2010 -	02/2011
99	JIND-SONEPAT (NL),NR - [220100280	01/2004	190.81 -	500.00	414.03	03/2012 -	12/2012
100	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	355.38 -	1,100.00	254.10	- -	03/2013
101	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	1,185.00	219.71	- 09/2009	12/2011
102	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	243.40	248.79	02/2009 02/2009	04/2013
103	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	4,444.00	911.23	03/2011 -	03/2016
104	KOSI BRIDGE (NL), ECR - [220100304	04/2002	323.41 -	341.41	272.26	03/2012 -	03/2013

(Aug,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
105	KODERMA GIRIDH (NL), ECR - [220100306	04/1996	371.36 -	768.87	415.19	- -	03/2010
106	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	792.32	03/2009 -	12/2012
107	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	1,514.74	10/2007 -	12/2012
108	DANIAWAN-BIHARSARIF (NL), ECR - [220100311	04/2001	104.79 -	406.92	78.91	- -	-
109	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314	04/2001	727.13 727.13	1,225.00	232.01	- -	-
110	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR [220100315	01/2004	915.70 -	1,717.29	1,343.13	- -	03/2013
111	BILASPUR-URKURA (DL) - [220100321	04/1997	151.52 -	350.00	321.48	- 03/2009	03/2011
112	RUPSA-BANGRIPOSI (GC)(SER) - [220100323	02/1996	57.94 -	639.97	174.53	03/1998 08/2005	08/2005
113	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	585.93	194.91	- -	12/2013
114	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	818.29	72.97	02/2015 -	-
115	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	225.00	212.13	03/2009 03/2009	04/2013
116	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	726.96 -	810.78	113.80	- -	03/2013
117	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329	04/2003	136.62 -	221.90	231.38	12/2007 03/2010	12/2010
118	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	114.01 283.95	477.88	392.05	03/2012 -	03/2013
119	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027	04/2005	240.00 -	355.00	401.42	03/2009 12/2009	03/2011
120	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032	04/2006	378.56 -	791.60	0.76	- -	-
121	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045	03/1997	186.92 -	261.70	56.12	02/2006 -	12/2013
122	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049	07/2006	743.00 -	1,117.11	-	03/2008 06/2008	-
123	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS&PU [N22000052	04/2003	98.74 -	337.30	222.07	- -	03/2012
124	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053	03/2005	470.09 -	1,417.97	1,011.09	- -	03/2012
125	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075	09/2006	324.90 -	385.54	226.12	03/2010 -	03/2012
126	PANSPURA-KHARAGPUR 3D LINE - [N22000076	09/2007	252.50 -	529.23	225.10	02/2010 -	12/2015
127	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI [N22000079	09/2007	404.19 -	900.00	253.14	- -	-

(Aug,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
128	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	900.00	542.57	- -	12/2012
129	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	453.04	392.26	03/2011 -	03/2011
130	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR - [N22000083]	09/1996	156.00 -	415.73	240.93	- -	03/2012
131	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 -	227.40	36.48	- -	-
132	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	582.83	129.43	- -	-
133	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR [N22000086]	09/2006	200.00 -	385.20	112.60	- -	03/2014
134	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	300.00 -	532.87	39.45	- -	-
135	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	820.40	150.01	03/2010 -	06/2014
136	BARDHAMAN-KATWA (GC) - [N22000091]	04/2007	245.15 -	1,106.62	207.07	12/2010 -	03/2011
137	MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N22000093]	04/2003	3,125.20 -	4,501.80	4,334.00	06/2011 -	03/2012
138	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]	12/2004	129.17 -	250.00	227.48	03/2011 -	03/2012
139	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,086.41	426.22	06/2005 -	06/2016
140	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	1,141.75	407.49	03/2014 -	03/2014
141	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,393.48	11.78	04/2014 -	03/2015
142	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	359.86	1.22	- -	03/2015
143	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	3,380.58	52.63	12/2015 -	12/2015
144	Ramanagram-Mysore doubling with electrification of Kengesii- Musore (SWR) - [N22000107]	04/2007	482.00 -	482.70	384.35	03/2013 -	03/2014
145	New Work for Construction of Metro railway from Joka to Binoy Badal Dinesh Bagh. - [N22000111]	04/2010	2,619.02 -	2,913.51	151.51	03/2016 -	03/2016
146	Jaipur - Ringus - Churu and Sikar - Loharu Gauge Conversion (NWR) - [N22000113]	04/2008	653.19 -	653.46	175.60	03/2014 -	03/2014
147	Dakshin-barasal-lakshmikantapur - [N22000116]	04/2009	259.51 -	533.38	85.44	12/2011 -	02/2012
148	Ghutiasharif-Canning (ER) - [N22000117]	04/2009	189.97 -	611.03	105.94	12/2011 -	11/2013
149	Pandabeswar-Chinpai doubling (ER) - [N22000118]	04/2004	225.68 -	293.74	136.74	12/2010 -	12/2010
150	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]	04/2008	394.14 -	404.39	0.49	03/2013 -	-
151	Bhuj-Naliya(GC) with extension from naliya to Vayor (WR) - [N22000123]	04/2008	318.24 -	468.62	1.00	03/2012 -	-

(Aug,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
152	Bhavnagar-workshop facilities for 50 BG coaches POH per month (WR) - [N22000125	04/2006	117.36 196.95	196.95	181.64	03/2011	-
153	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project - [N22000127	04/1996	1,676.31 -	4,255.37	3,161.45	03/2009	12/2013
	Total		42,495.77 -	282,440.72	173,267.99		
<u>Road Transport & Highways</u>							
154	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153	04/2000	225.00 -	241.53	132.10	04/2004	09/2012
155	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221	12/2003	155.00 -	201.66	128.88	09/2008	03/2013
156	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236	12/2003	166.27 -	193.10	163.41	03/2008	10/2012
157	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237	12/2003	284.00 -	359.00	216.44	05/2008	03/2013
158	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	60.42	04/2009	07/2013
159	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	92.32	11/2008	07/2013
160	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061	12/2003	212.00 -	386.10	26.30	09/2007	03/2013
161	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	363.74	49.25	07/2009	04/2014
162	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	179.23	02/2010	12/2013
163	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098	12/2003	348.16 -	465.50	178.61	09/2007	06/2013
164	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133	05/2009	1,108.00 -	2,288.00	3,460.60	11/2011	08/2013
	Total		3,324.28 -	287,885.92	177,955.55		
<u>Shipping & Ports</u>							
165	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL - [N25000003	10/2005	800.00 -	1,571.60	5.75	10/2008	10/2008
166	DEEPENING OF CHEENEL AT PARADIP PORT - [N25000004	12/2005	154.84 -	253.36	-	- 01/2009	01/2009
167	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016	11/2007	1,228.00 -	1,460.00	841.40	12/2010	10/2013
168	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	110.00	03/2006	06/2013
169	Construction of berthing and allied facilities off Tekra near Tuna,Kandla Port Trust - [N25000037	04/2005	882.00 -	1,060.00	0.93	02/2011	12/2012
170	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039	12/2005	702.00 -	755.50	219.00	03/2011	03/2013

(Aug,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
171	Acquisition of two nos. of 120 B.P BY 079& 080 - [N25000042	04/2009	290.85	305.00	197.14	06/2011	09/2012
172	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN - [N25000048	03/2009	3,500.00	4,150.00	3,433.40	01/2012	12/2012
173	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers from M/S Jiangsu Eastern Heavy Industries - [N25000051	08/2010	612.72	627.64	214.65	12/2012	05/2013
174	Acquisition of two(2) Nos. of 317000 DWT very large crude carriers from M/S Jiangsu rongsheng heavy - [N25000053	10/2010	966.46	994.82	248.23	02/2014	02/2014
175	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059	03/2007	245.67	373.22	326.08	04/2009	02/2011
	Total		9,532.54	300,037.06	183,552.13		
			-				
	<u>Steel</u>						
176	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067	10/2005	8,692.00	12,291.00	9,726.00	10/2009	03/2013
177	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018	01/2007	295.89	607.17	339.69	12/2011	10/2012
178	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038	08/2007	108.00	216.68	91.83	10/2012	12/2012
179	EXPANSION OF IISCO STEEL PLANT - [N12000051	02/2008	14,443.00	16,408.00	13,628.33	12/2011	12/2012
180	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREMENT EXP. UNIT - [N12000068	07/2007	230.00	343.58	248.53	02/2011	12/2012
181	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069	07/2007	260.00	350.00	246.19	08/2010	10/2012
	Total		24,028.89	330,253.49	207,832.70		
			-				
	<u>Telecommunications</u>						
182	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058	01/2009	149.15	158.72	76.70	06/2009	12/2012
183	GSM equipment of 1625000Lines (2G) 325000 lines 3(G) MP Phase V.1 Telecom Circle - [N26000090	11/2009	916.70	930.60	805.75	11/2010	11/2012
	Total		1,065.85	331,342.81	208,715.15		
			-				
	<u>Urban Development</u>						
184	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00	11,609.00	2,267.57	12/2011	03/2013
185	C/o office building for IDBI at bandra Kurla Complex, Mumbai - [N28000048	11/2006	114.18	173.08	-	04/2009	-
			173.08				

(Aug,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		6,509.18	343,124.89	210,982.72		
			-				
	<u>Water Resources</u>						
186	PAGLADIYA DAM PROJECT	01/2001	542.90	1,187.00	35.49	12/2007	12/2012
	- [300100001		-			-	
	Total		542.90	344,311.89	211,018.21		
			-				
	Grand Total		214,801.53	2,639,075.40	1,672,441.35		

List of ongoing projects having time and cost overrun w.r.to original

(Aug,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apxenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Atomic Energy</u>						
1	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	14,945.00	12/2008 -	03/2013
	Total		13,171.00 -	17,270.00	14,945.00		
	<u>Civil Aviation</u>						
2	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]	08/2008	1,942.51 -	2,325.00	2,081.48	05/2011 -	10/2012
	Total		1,942.51 -	19,595.00	17,026.48		
	<u>Coal</u>						
3	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,027.59	2,460.35	06/2009 -	03/2013
4	MAGADH OC (CCL) - [N06000015]	07/2006	469.78 -	706.40	19.23	07/2012 -	03/2016
5	ADRIYALA SHAFT PROJECT - [N06000016]	09/2006	212.34 -	779.26	310.04	03/2013 -	10/2014
6	TUTICORIN THERMAL POWER PROJECT - [N06000047]	05/2008	4,904.54 -	4,909.54	3,296.75	03/2012 -	03/2014
	Total		7,617.44 -	29,017.79	23,112.85		
	<u>Petroleum</u>						
7	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]	09/2001	345.10 -	663.69	629.66	03/2007 -	03/2014
8	IOR GELEKI (ONGCL) - [160100216]	09/2001	390.09 -	1,674.11	1,535.19	03/2007 -	03/2017
9	IOR, RUDRASAGAR (ONGCL) - [160100217]	09/2001	113.90 -	438.85	269.29	03/2006 -	03/2013
10	DEV OF G1 AND GS-15 (ONGCL) - [160100231]	04/2003	429.82 -	2,735.65	2,184.00	04/2006 -	06/2013
11	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]	08/2006	3,195.16 -	3,690.37	2,520.91	12/2008 -	04/2013
12	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]	01/2007	2,853.29 -	6,326.40	5,557.03	05/2010 -	10/2012
13	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]	01/2007	2,323.40 -	2,920.82	1,858.42	09/2010 03/2012	04/2013
14	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]	06/2007	3,248.78 -	5,633.44	3,761.86	08/2010 03/2012	12/2013
15	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]	10/2007	5,713.03 -	8,813.41	7,084.38	05/2010 -	03/2013
16	North Tapti Gas Field Development - [N16000096]	07/2008	589.70 755.56	755.76	677.99	03/2011 -	03/2013

(Aug,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		19,202.27	62,670.29	49,191.58		
			-				
	<u>Power</u>						
17	PARBATI HEP (NHPC) II - [180100210	09/2002	3,919.59	5,366.00	3,532.32	09/2009	12/2017
			-			-	
18	SUBANSIRI LOWER H.E.P (NHPC) - [180100221	09/2003	6,285.33	10,667.00	5,733.74	09/2010	03/2017
			-			-	
19	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC) [180100222	10/2003	768.92	1,628.00	1,551.34	03/2007	01/2013
			-			-	
20	BARH STPP(3X660MW) NTPC - [180100242	12/2003	8,692.97	8,693.00	7,288.00	12/2009	03/2016
			-			-	
21	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243	09/2005	1,061.38	1,501.75	1,173.29	09/2009	08/2013
			-			-	
22	PARBATI H.E.P. STAGE -III (NHPC) - [180100250	10/2005	2,304.56	2,716.00	1,893.71	10/2010	06/2013
			-			-	
23	URI H.E.P STAGE -II (NHPC) - [180100251	08/2005	1,729.29	2,083.00	1,772.30	11/2009	03/2013
			-			-	
24	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258	05/2005	1,779.29	2,159.07	1,833.11	09/2008	12/2012
			-			-	
25	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006	08/2006	611.01	936.00	786.38	08/2010	01/2013
			-			-	
26	CHUTAK HYDRO-ELECTRIC PROJECT - [N18000007	08/2006	621.26	913.00	751.21	02/2011	10/2012
			-			-	
27	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	07/2006	1,657.00	2,978.86	371.17	07/2010	02/2016
			-			-	
28	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP [N18000018	07/2006	557.24	758.75	589.00	01/2010	02/2013
			-			-	
29	KISHANGANGA HEP - [N18000031	07/2007	2,238.67	3,642.00	1,630.50	01/2016	11/2016
			-			-	
30	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT [N18000042	08/2008	2,491.58	3,422.44	316.25	07/2014	05/2016
			-			-	
31	MOUDA STPP - [N18000048	11/2008	5,459.28	6,010.89	4,349.00	08/2012	03/2013
			-			-	
32	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064	04/2008	297.37	386.32	328.83	07/2011	11/2012
			-			-	
	Total		40,474.74	116,532.37	83,091.73		
			-				
	<u>Railways</u>						
33	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009	03/1984	520.00	634.13	555.27	03/1995	03/2013
			422.79			-	
34	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00	8,000.00	8,069.06	03/2001	12/2017
			-			-	
35	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148	04/1993	100.00	227.94	202.02	03/2002	03/2013
			119.29			-	
36	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	401.81	495.44	191.30	03/2004	03/2014
			-			-	

(Aug,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
37	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168	04/1995	184.00 -	900.05	565.12	12/2011 12/2010	03/2013
38	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190	04/1996	157.00 -	333.50	210.82	03/2012 -	10/2012
39	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201	09/1997	1,000.00 -	3,230.01	2,408.10	04/2008 12/2011	12/2015
40	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	31.42 154.30	499.16	168.27	03/2007 03/2007	03/2015
41	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	456.45	293.29	06/2004 -	12/2012
42	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR [220100240	04/1997	233.00 335.77	1,043.55	659.06	03/2012 -	02/2013
43	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241	07/1998	248.44 -	1,115.21	877.21	12/2012 -	01/2013
44	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	100.00 -	1,041.79	730.92	12/2010 -	03/2015
45	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	1,655.81	1,275.88	12/2008 -	03/2014
46	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	260.85	02/2011 -	02/2013
47	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	138.00 240.59	607.09	407.33	12/2012 12/2012	02/2013
48	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	1,412.74	448.10	03/2005 12/2008	06/2016
49	JIND-SONEPAT (NL),NR - [220100280	01/2004	190.81 -	500.00	414.03	03/2012 -	12/2012
50	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	243.40	248.79	02/2009 02/2009	04/2013
51	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	4,444.00	911.23	03/2011 -	03/2016
52	KOSI BRIDGE (NL), ECR - [220100304	04/2002	323.41 -	341.41	272.26	03/2012 -	03/2013
53	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	792.32	03/2009 -	12/2012
54	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	1,514.74	10/2007 -	12/2012
55	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	225.00	212.13	03/2009 03/2009	04/2013
56	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	114.01 283.95	477.88	392.05	03/2012 -	03/2013
57	GOELKERA-MANOHARPUR,(LD)(SER) - [N220000045	03/1997	186.92 -	261.70	56.12	02/2006 -	12/2013
58	PANSPURA-KHARAGPUR 3D LINE - [N220000076	09/2007	252.50 -	529.23	225.10	02/2010 -	12/2015
59	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N220000088	04/2006	325.00 -	820.40	150.01	03/2010 -	06/2014
60	TAMLUK DIGHA,LINE DOUBLING (SER) - [N220000097	03/1984	293.97 -	1,086.41	426.22	06/2005 -	06/2016
61	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	619.34 -	2,393.48	11.78	04/2014 -	03/2015

(Aug,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
62	Ramanagram-Mysore doubling with electrification of Kengesii- Musore (SWR) - [N22000107	04/2007	482.00 -	482.70	384.35	03/2013 -	03/2014
63	Ghutiasharif-Canning (ER) - [N22000117	04/2009	189.97 -	611.03	105.94	12/2011 -	11/2013
64	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project - [N22000127	04/1996	1,676.31 -	4,255.37	3,161.45	03/2009 -	12/2013
	Total		13,972.11 -	160,411.25	109,692.85		
Road Transport & Highways							
65	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153	04/2000	225.00 -	241.53	132.10	04/2004 -	09/2012
66	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221	12/2003	155.00 -	201.66	128.88	09/2008 -	03/2013
67	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236	12/2003	166.27 -	193.10	163.41	03/2008 -	10/2012
68	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237	12/2003	284.00 -	359.00	216.44	05/2008 -	03/2013
69	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	60.42	04/2009 -	07/2013
70	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	92.32	11/2008 -	07/2013
71	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061	12/2003	212.00 -	386.10	26.30	09/2007 -	03/2013
72	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	363.74	49.25	07/2009 -	04/2014
73	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	179.23	02/2010 -	12/2013
74	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098	12/2003	348.16 -	465.50	178.61	09/2007 -	06/2013
75	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133	05/2009	1,108.00 -	2,288.00	3,460.60	11/2011 -	08/2013
	Total		3,324.28 -	165,856.45	114,380.41		
Shipping & Ports							
76	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016	11/2007	1,228.00 -	1,460.00	841.40	12/2010 -	10/2013
77	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	110.00	03/2006 -	06/2013
78	Construction of berthing and allied facilities off Tekra near Tuna,Kandla Port Trust - [N25000037	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012
79	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013
80	Acquisition of two nos. of 120 B.P BY 079& 080 - [N25000042	04/2009	290.85 -	305.00	197.14	06/2011 -	09/2012

(Aug,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
81	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN - [N25000048]	03/2009	3,500.00	4,150.00	3,433.40	01/2012	12/2012
82	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers from M/S Jiangsu Eastern Heavy Industries - [N25000051]	08/2010	612.72	627.64	214.65	12/2012	05/2013
	Total		7,365.57	174,814.59	119,396.93		
			-				
	<u>Steel</u>						
83	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]	10/2005	8,692.00	12,291.00	9,726.00	10/2009	03/2013
84	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]	01/2007	295.89	607.17	339.69	12/2011 06/2010	10/2012
85	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]	08/2007	108.00	216.68	91.83	10/2012	12/2012
86	EXPANSION OF IISCO STEEL PLANT - [N12000051]	02/2008	14,443.00	16,408.00	13,628.33	12/2011	12/2012
87	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT EXP. UNIT - [N12000068]	07/2007	230.00	343.58	248.53	02/2011	12/2012
88	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]	07/2007	260.00	350.00	246.19	08/2010	10/2012
	Total		24,028.89	205,031.02	143,677.50		
			-				
	<u>Telecommunications</u>						
89	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058]	01/2009	149.15	158.72	76.70	06/2009	12/2012
90	GSM equipment of 1625000Lines (2G) 325000 lines 3(G) MP Phase V.1 Telecom Circle - [N26000090]	11/2009	916.70	930.60	805.75	11/2010	11/2012
	Total		1,065.85	206,120.34	144,559.95		
			-				
	<u>Urban Development</u>						
91	BANGALORE METRO RAIL PROJECT - [N28000008]	05/2006	6,395.00	11,609.00	2,267.57	12/2011	03/2013
	Total		6,395.00	217,729.34	146,827.52		
			-				
	<u>Water Resources</u>						
92	PAGLADIYA DAM PROJECT - [300100001]	01/2001	542.90	1,187.00	35.49	12/2007	12/2012
	Total		542.90	218,916.34	146,863.01		
			-				
	Grand Total		139,102.56	1,593,964.78	1,112,765.81		

Abbreviations used in the report

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro
LEP	Life Extension Program
LOI	Letter of Intent

LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECF	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SSS	Sardar Swaran Singh
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
